| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Construction Baseline Schedule** | | | | | | |
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13* | | 0 |
| CM-1002 | CM - Contract Time (578 Cal Days) | 579 | 579 | 06-Mar-13 | 05-Oct-14 | 0 |
| CM-1014 | CM - Start of Construction | 0 | 0 | 03-Apr-13 | | 0 |
| CM-1006 | CM - Construction Documents Issued by Client - (w/i | 0 | 0 | 04-Jul-13* | | 0 |
| CM-1008 | CM - Finalization of Allowances - (w/i 180 Days of NTF | 0 | 0 | 02-Sep-13* | | 0 |
| CO-7004 | CO - Prep / Submit O&M Manuals | 40 | 40 | 28-Jun-14 | 06-Aug-14 | 0 |
| CO-7000 | CO - City of Bellevue TCO | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 0 |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 23-Aug-14 | | 2 |
| CM-1016 | CM - Owner FF+E "Build-Out" | 42 | 42 | 25-Aug-14 | 05-Oct-14 | 0 |
| CO-7002 | CO - Final Inspections | 20 | 20 | 05-Sep-14 | 02-Oct-14 | 0 |
| CM-1018 | CM - Hotel Operations Training | 21 | 21 | 15-Sep-14 | 05-Oct-14 | 0 |
| CO-7006 | CO - Certificate of Occupancy | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 0 |
| CM-1022 | CM - Building Turnover | 0 | 0 | | 03-Oct-14 | 2 |
| CM-1024 | CM - Substantial Completion / Hotel Opening - (CCD) | 0 | 0 | | 05-Oct-14* | 0 |
| **Misc Milestones** | | | | | | |
| CM-1020 | MM - Site Mobilization | 10 | 10 | 06-Mar-13 | 15-Mar-13 | 11 |
| MM-1004 | MM - TopOut - Podium | 0 | 0 | | 11-Dec-13 | 5 |
| MM-1000 | MM - Start Rough In Tower | 0 | 0 | 31-Dec-13 | | 72 |
| MM-1006 | MM - Top Out - Tower / Structure | 0 | 0 | | 28-Mar-14 | 38 |
| MM-1008 | MM - Permanent Power Available | 0 | 0 | | 08-Apr-14 | 89 |
| MM-1002 | MM - Start Drywall In Tower | 0 | 0 | 24-Apr-14 | | 0 |
| CM-1010 | MM - Mock Unit Complete | 0 | 0 | | 09-Jun-14 | 3 |

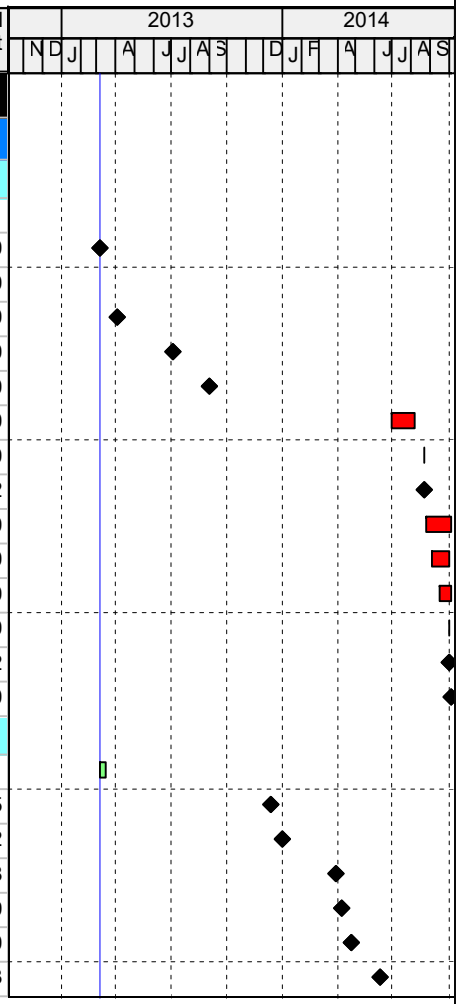


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 18-Jul-14 | 54 |
| **Executive Summary** | | | | | | |
| ES-1000 | Foundation / SubStructure - (Levels LL4 / LL3) | 111 | 111 | 03-Apr-13 | 10-Sep-13 | 96 |
| ES-1002 | Lower Podium Structure - (LL2 / LL1 / L1 / L2) | 95 | 95 | 08-Aug-13 | 24-Dec-13 | 19 |
| ES-1006 | Lower Podium RI's - (LL2 / LL1 / L1 / L2) | 164 | 164 | 13-Aug-13 | 08-Apr-14 | 56 |
| ES-1004 | Upper Tower Structure - (Levels 3 Thru PH) | 85 | 85 | 12-Dec-13 | 14-Apr-14 | 26 |
| ES-1016 | Metal Wall Panels @ Podium | 37 | 37 | 23-Dec-13 | 14-Feb-14 | 0 |
| ES-1008 | Upper Tower RI's - (Levels 3 Thru PH) | 99 | 99 | 07-Jan-14 | 27-May-14 | 49 |
| ES-1018 | Curtainwall | 24 | 24 | 14-Jan-14 | 14-Feb-14 | 76 |
| ES-1010 | Elevators | 137 | 137 | 07-Feb-14 | 20-Aug-14 | 30 |
| ES-1020 | Windows | 80 | 80 | 24-Feb-14 | 16-Jun-14 | 25 |
| ES-1024 | EIFS Wall Panels - (Not Including Hold Out Panels) | 76 | 76 | 03-Mar-14 | 17-Jun-14 | 28 |
| ES-1012 | Lower Podium Finishes - (LL2 / LL1 / L1 / L2) | 87 | 87 | 10-Mar-14 | 10-Jul-14 | 31 |
| ES-1014 | Upper Tower Finishes - (Levels 3 Thru PH) | 117 | 117 | 21-Apr-14 | 03-Oct-14 | 0 |
| ES-1022 | Start-Up / Testing / Commissioning | 60 | 60 | 09-Jul-14 | 01-Oct-14 | 0 |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| **Tower Crane** | | | | | | |
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 5 | 11-Jun-13 | 17-Jun-13 | 15 |
| TC-5902 | Tower Crane - Erectiion | 2 | 2 | 18-Jun-13 | 19-Jun-13 | 15 |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 1 | 20-Jun-13 | 20-Jun-13 | 25 |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 21-Jun-13 | | 25 |
| TC-5906 | Tower Crane - Operatational Period | 395 | 395 | 21-Jun-13 | 20-Jul-14 | 32 |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 24 |
| **Man & Material Lifts** | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 5 | 14-Oct-13 | 18-Oct-13 | 233 |
| ML-5952 | Man/Material Lifts - Start Erectiion | 5 | 5 | 21-Oct-13 | 25-Oct-13 | 236 |
| ML-5954 | Man/Material Lifts - Load Test / Certify | 2 | 2 | 26-Oct-13 | 27-Oct-13 | 343 |

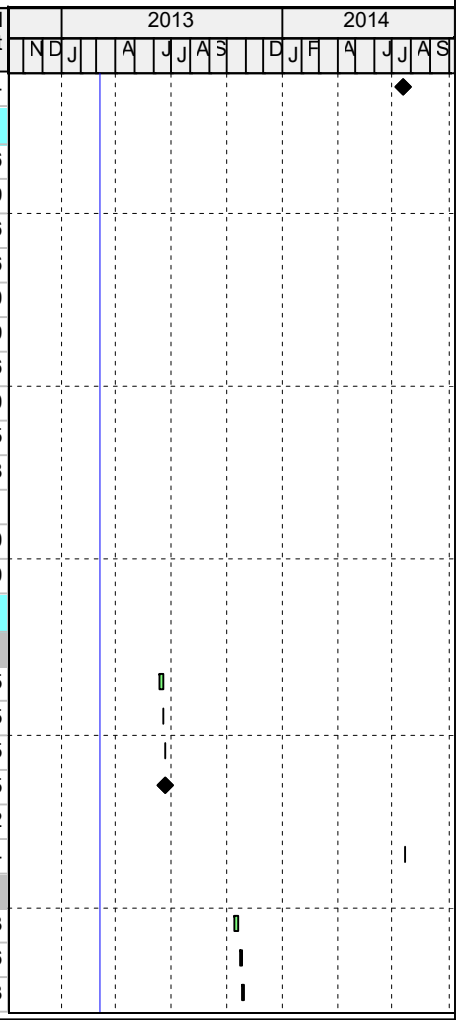



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 28-Oct-13 | | 343 |
| ML-5958 | Man/Material Lifts - Operatational Period | 262 | 262 | 28-Oct-13 | 16-Jul-14 | 36 |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 5 | 5 | 17-Jul-14 | 23-Jul-14 | 26 |
| **Pre-Construction** | | | | | | |
| **Permits** | | | | | | |
| WDOE NPDES Permit | | | | | | |
| PC-5034 | Submit WDOE NPDES Permit | 1 | 0 | 20-Sep-12 A | 20-Sep-12 A | |
| PC-5036 | Review/approve WDOE NPDES Permit | 18 | 0 | 20-Sep-12 A | 29-Oct-12 A | |
| Right of Way Permit | | | | | | |
| PC-5000 | Submit ROW Permit | 1 | 0 | 03-Aug-12 A | 03-Aug-12 A | |
| PC-5002 | Review/Approve ROW Permit | 18 | 0 | 03-Aug-12 A | 29-Oct-12 A | |
| Clear & Grade Permit | | | | | | |
| PC-5004 | Submit Clear and Grade Permit | 1 | 0 | 03-Aug-12 A | 03-Aug-12 A | |
| PC-5006 | Review/Approve Clear and Grade Permit | 18 | 0 | 03-Aug-12 A | 02-Nov-12 A | |
| Shoring Permit | | | | | | |
| PC-5008 | Submit Shoring Permit | 1 | 0 | 03-Aug-12 A | 03-Aug-12 A | |
| PC-5010 | Review/Approve Shoring Permit | 18 | 0 | 03-Aug-12 A | 05-Nov-12 A | |
| Below Grade Structure Permit | | | | | | |
| PC-5014 | Review/Approve Below Grade Structural Permit | 45 | 5 | 25-Sep-12 A | 12-Mar-13 | 65 |
| PC-5012 | Submit Below Grade Structural Permit | 1 | 0 | 02-Oct-12 A | 02-Oct-12 A | |
| Superstructure Permit | | | | | | |
| PC-5016 | Submit Superstructure Permit | 1 | 0 | 02-Oct-12 A | 02-Oct-12 A | |
| PC-5018 | Review/Approve Superstructure Permit | 45 | 5 | 03-Oct-12 A | 12-Mar-13 | 247 |
| Above Grade Architectural Permit | | | | | | |
| PC-5020 | Submit Architectural Permit | 5 | 5 | 08-Jul-13 | 12-Jul-13 | 57 |
| PC-5022 | Review/Approve Architectural Permit | 40 | 40 | 15-Jul-13 | 09-Sep-13 | 57 |
| Deferred Permits | | | | | | |

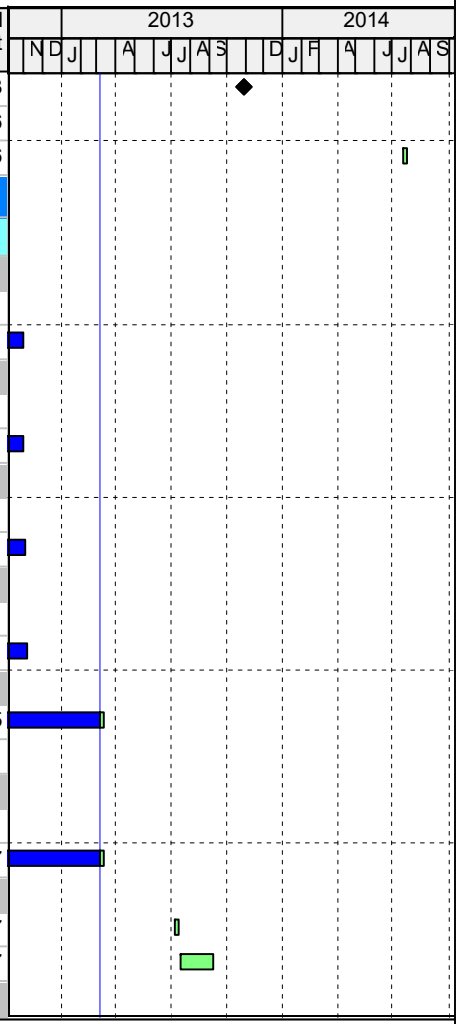


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PC-5026 | Submit Smoke Control Permit | 65 | 0 | 03-Oct-12 A | 03-Oct-12 A | |
| PC-5032 | Submit Elect Service To PSE | 60 | 60 | 12-Mar-13 | 05-Jun-13 | 247 |
| PC-5024 | Signage Permit | 25 | 25 | 08-Jul-13 | 09-Aug-13 | 290 |
| **Submittals** | | | | | | |
| Prepare / Submit Submittals | | | | | | |
| PC-5028 | Subcontract Agreements & Submittals | 80 | 80 | 06-Mar-13 | 26-Jun-13 | 5 |
| Review / Approve Submittals | | | | | | |
| PC-5030 | Review / Approve Submittals | 100 | 100 | 03-Apr-13 | 23-Aug-13 | 280 |
| **Material / Equipment Procurement** | | | | | | |
| PC-5038 | MM - Soil Nail Procurement | 28 | 28 | 06-Mar-13 | 02-Apr-13 | 0 |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |
| Mass Excavation / Shoring | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 3 | 27-Mar-13 | 02-Apr-13 | 0 |
| SW-2002 | Demolition And Utility Relocation | 8 | 8 | 27-Mar-13 | 10-Apr-13 | 0 |
| Site Finishes | | | | | | |
| SW-2004 | Utility Connections | 30 | 30 | 26-Feb-14 | 08-Apr-14 | 56 |
| SW-2006 | Install Perm Power Electrical Service | 20 | 20 | 12-Mar-14 | 08-Apr-14 | 56 |
| SW-2008 | Sidewalks / Landscaping / Street Improvements | 40 | 40 | 09-Apr-14 | 04-Jun-14 | 56 |
| **Structure** | | | | | | |
| Foundation / Substructure - (Levels LL4 / LL3) | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |
| LL4-1600 | LL4 - Excavation / Soil Nail Walls / Dewatering | 50 | 50 | 03-Apr-13 | 17-Jun-13 | 0 |
| LL4-1601 | LL4 - Excavate Footings | 14 | 14 | 11-Jun-13 | 28-Jun-13 | 0 |
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 15 | 12-Jun-13 | 02-Jul-13 | 0 |
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 5 | 18-Jun-13 | 24-Jun-13 | 9 |

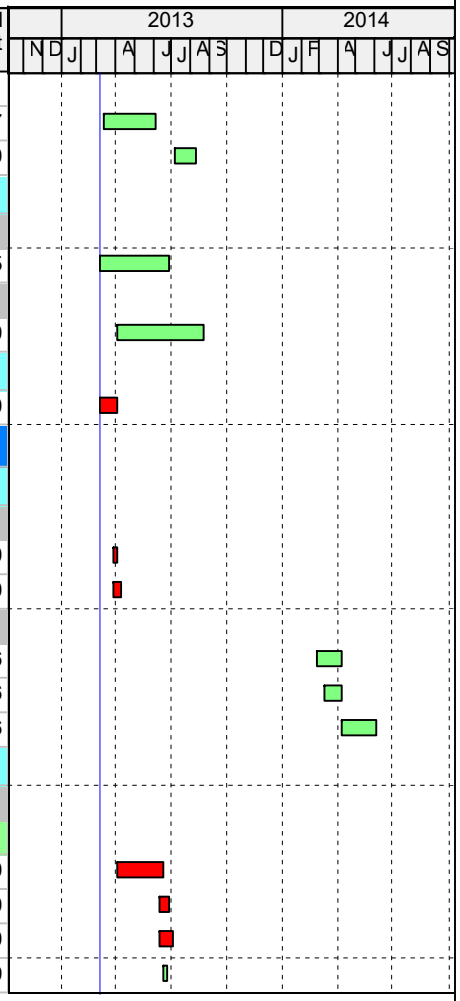



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-1606 | LL4 - Undrgrnd Plumbing | 5 | 5 | 18-Jun-13 | 24-Jun-13 | 9 |
| LL4-1608 | LL4 - Undrgrnd Elec | 5 | 5 | 18-Jun-13 | 24-Jun-13 | 9 |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 5 | 19-Jun-13 | 25-Jun-13 | 10 |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 10 | 26-Jun-13 | 11-Jul-13 | 0 |
| LL4-2033 | LL4 - Shotcrete Walls | 9 | 9 | 26-Jun-13 | 10-Jul-13 | 1 |
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 5 | 03-Jul-13 | 11-Jul-13 | 117 |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 3 | 03-Jul-13 | 09-Jul-13 | 0 |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 3 | 03-Jul-13 | 09-Jul-13 | 0 |
| LL4-1614 | LL4 - FRP SOG | 5 | 5 | 10-Jul-13 | 16-Jul-13 | 0 |
| LL4-2004 | LL4 - Shore / Form Deck LL3 (Above) | 6 | 6 | 16-Jul-13 | 23-Jul-13 | 0 |
| LL4-2006 | LL4 - M & E Inserts LL3 (Above) | 4 | 4 | 18-Jul-13 | 23-Jul-13 | 2 |
| LL4-2008 | LL4 - ReSteel / PT Cables LL3 (Above) | 6 | 6 | 18-Jul-13 | 25-Jul-13 | 0 |
| LL4-2012 | LL4 - Pour / Finish Deck LL3 (Above) | 1 | 1 | 26-Jul-13 | 26-Jul-13 | 0 |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 2 | 29-Jul-13 | 30-Jul-13 | 106 |
| LL4-1618 | LL4 - FRP Ramp SOG | 3 | 3 | 31-Jul-13 | 02-Aug-13 | 106 |
| LL4-2014 | LL4 - Stress Tendons LL3 (Above) | 1 | 1 | 01-Aug-13 | 01-Aug-13 | 0 |
| LL4-2016 | LL4 - Strip / ReShore Deck LL3 (Above) | 3 | 3 | 02-Aug-13 | 06-Aug-13 | 0 |
| LL4-2018 | LL4 - Remove Shoring | 4 | 4 | 07-Aug-13 | 12-Aug-13 | 112 |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2001 | LL3 - Waterproof Walls | 3 | 3 | 24-Jul-13 | 26-Jul-13 | 7 |
| LL3-2002 | LL3 - FRP Columns / Misc Walls | 8 | 8 | 29-Jul-13 | 07-Aug-13 | 0 |
| LL3-2000 | LL3 - FRP Core Walls | 8 | 8 | 29-Jul-13 | 07-Aug-13 | 3 |
| LL3-2033 | LL3 - Shotcrete Walls | 9 | 9 | 29-Jul-13 | 08-Aug-13 | 3 |
| LL3-2004 | LL3 - Shore / Form Deck LL2 (Above) | 6 | 6 | 07-Aug-13 | 14-Aug-13 | 0 |
| LL3-2006 | LL3 - M & E Inserts LL2 (Above) | 4 | 4 | 09-Aug-13 | 14-Aug-13 | 2 |
| LL3-2008 | LL3 - ReSteel / PT Cables LL2 (Above) | 6 | 6 | 09-Aug-13 | 16-Aug-13 | 0 |
| LL3-2010 | LL3 - Install Embeds LL2 (Above) | 2 | 2 | 09-Aug-13 | 12-Aug-13 | 4 |

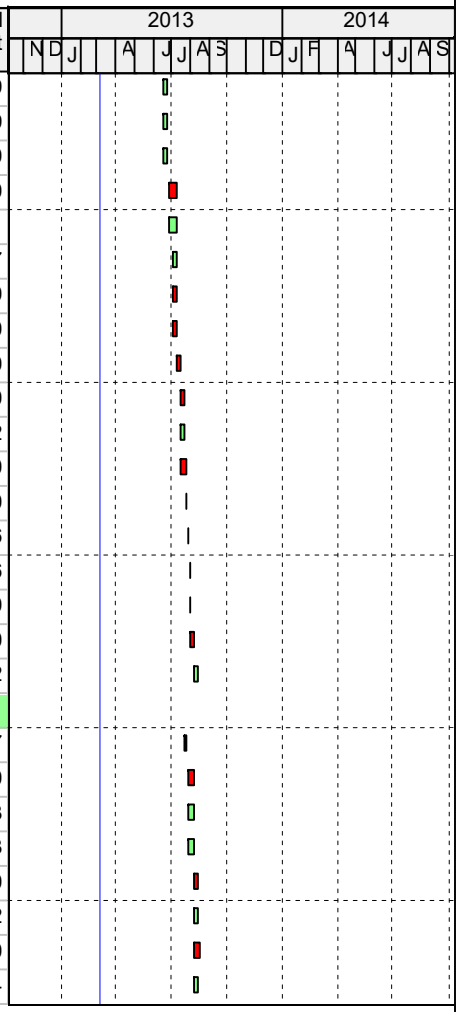



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-2012 | LL3 - Pour / Finish Deck LL2 (Above) | 1 | 1 | 19-Aug-13 | 19-Aug-13 | 0 |
| LL3-2013 | LL3 - Pour / Finish Ramp | 1 | 1 | 20-Aug-13 | 20-Aug-13 | 95 |
| LL3-2014 | LL3 - Stress Tendons LL2 (Above) | 1 | 1 | 23-Aug-13 | 23-Aug-13 | 93 |
| LL3-2016 | LL3 - Strip / ReShore Deck LL2 (Above) | 3 | 3 | 26-Aug-13 | 28-Aug-13 | 93 |
| LL3-2020 | LL3 - Waterproof Walls @ 10 Line | 2 | 2 | 29-Aug-13 | 30-Aug-13 | 93 |
| LL3-2022 | LL3 - Backfill @ 10 Line | 2 | 2 | 03-Sep-13 | 04-Sep-13 | 93 |
| LL3-2018 | LL3 - Remove Shoring | 4 | 4 | 05-Sep-13 | 10-Sep-13 | 93 |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Grids 1 to 4 - (SOG @ Loading Dock)** | | | | | | |
| LL2-2001 | LL2 - Excavation @ Loading Dock | 3 | 3 | 08-Aug-13 | 12-Aug-13 | 0 |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 5 | 13-Aug-13 | 19-Aug-13 | 2 |
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls | 5 | 5 | 13-Aug-13 | 19-Aug-13 | 5 |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 4 | 13-Aug-13 | 16-Aug-13 | 6 |
| LL2-2020 | LL2 - Undrgmd Plumbing | 10 | 10 | 13-Aug-13 | 26-Aug-13 | 6 |
| LL2-2022 | LL2 - Undrgmd Elec | 10 | 10 | 13-Aug-13 | 26-Aug-13 | 6 |
| LL2-2021 | LL2 - FRP Elec Vault | 5 | 5 | 13-Aug-13 | 19-Aug-13 | 11 |
| LL2-2056 | LL2 - Grease Intercepter | 5 | 5 | 13-Aug-13 | 19-Aug-13 | 15 |
| LL2-2029 | LL2 - Ftgs & Foundations @ LL2 SOG | 8 | 8 | 13-Aug-13 | 22-Aug-13 | 0 |
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 3 | 20-Aug-13 | 22-Aug-13 | 2 |
| LL2-2011 | LL2 - FRP Loading Dock Ftgs / Fndtns | 5 | 5 | 20-Aug-13 | 26-Aug-13 | 0 |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 2 | 20-Aug-13 | 21-Aug-13 | 9 |
| LL2-2027 | LL2 - Waterproof Walls | 2 | 2 | 23-Aug-13 | 26-Aug-13 | 0 |
| LL2-2015 | LL2 - FRP Columns / Misc Walls | 6 | 6 | 27-Aug-13 | 04-Sep-13 | 0 |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 6 | 27-Aug-13 | 04-Sep-13 | 0 |
| LL2-2024 | LL2 - Cap Fill / Fine Grade | 4 | 4 | 05-Sep-13 | 10-Sep-13 | 0 |
| LL2-2017 | LL2 - FRP Loading Dock Lwr & Upr SOG's | 8 | 8 | 11-Sep-13 | 20-Sep-13 | 0 |

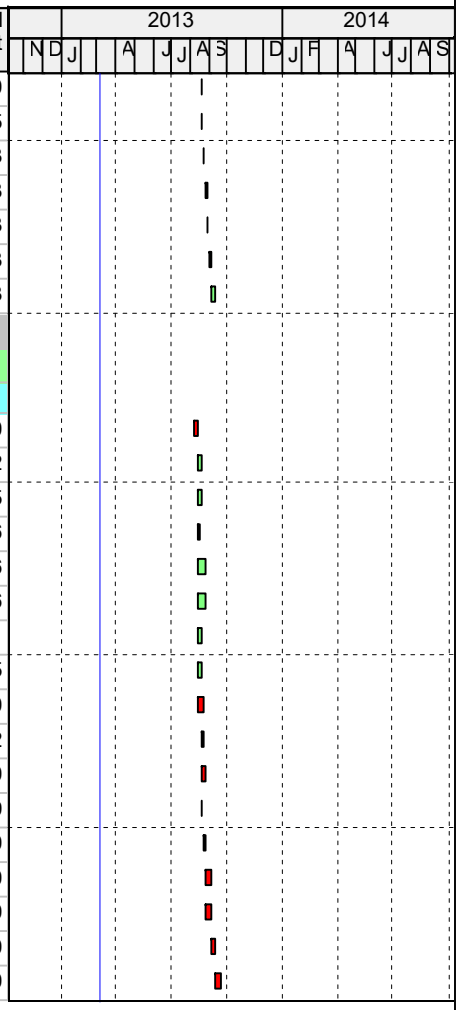



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2019 | LL2 - FRP Loading Dock Stairs | 4 | 4 | 23-Sep-13 | 26-Sep-13 | 92 |
| LL2-2044 | LL2 - Set Generator | 1 | 1 | 23-Sep-13 | 23-Sep-13 | 0 |
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 8 | 20-Aug-13 | 29-Aug-13 | 13 |
| LL2-2000 | LL2 - FRP Core Walls | 8 | 8 | 20-Aug-13 | 29-Aug-13 | 16 |
| LL2-2035 | LL2 - Shotcrete Walls | 8 | 8 | 20-Aug-13 | 29-Aug-13 | 20 |
| LL2-2023 | LL2 - Waterproof Walls | 3 | 3 | 30-Aug-13 | 04-Sep-13 | 13 |
| LL2-2004 | LL2 - Shore / Form Deck LL1 (Above) | 8 | 8 | 24-Sep-13 | 03-Oct-13 | 0 |
| LL2-2006 | LL2 - M & E Inserts LL1 (Above) | 4 | 4 | 26-Sep-13 | 01-Oct-13 | 3 |
| LL2-2008 | LL2 - ReSteel / PT Cables LL1 (Above) | 7 | 7 | 26-Sep-13 | 04-Oct-13 | 0 |
| LL2-2010 | LL2 - Install Embeds LL1 (Above) | 3 | 3 | 26-Sep-13 | 30-Sep-13 | 4 |
| LL2-2012 | LL2 - Pour / Finish Deck LL1 (Above) | 1 | 1 | 07-Oct-13 | 07-Oct-13 | 0 |
| LL2-2013 | LL2 - Pour / Finish Ramp | 1 | 1 | 08-Oct-13 | 08-Oct-13 | 2 |
| LL2-2014 | LL2 - Stress Tendons LL1 (Above) | 1 | 1 | 11-Oct-13 | 11-Oct-13 | 0 |
| LL2-2016 | LL2 - Strip / ReShore Deck LL1 (Above) | 3 | 3 | 14-Oct-13 | 16-Oct-13 | 0 |
| LL2-2018 | LL2 - Remove Shoring Grid Lid | 4 | 4 | 17-Oct-13 | 22-Oct-13 | 34 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| LL1-2020 | LL1 - Waterproof Walls | 3 | 3 | 05-Sep-13 | 09-Sep-13 | 23 |
| LL1-2002 | LL1 - FRP Columns / Misc Walls | 8 | 8 | 08-Oct-13 | 17-Oct-13 | 3 |
| LL1-2000 | LL1 - FRP Core Walls | 8 | 8 | 08-Oct-13 | 17-Oct-13 | 3 |
| LL1-2033 | LL1 - Shotcrete Walls | 8 | 8 | 08-Oct-13 | 17-Oct-13 | 3 |
| LL1-2004 | LL1 - Shore / Form Deck L1 (Above) | 8 | 8 | 17-Oct-13 | 28-Oct-13 | 0 |
| LL1-2006 | LL1 - M & E Inserts L1 (Above) | 4 | 4 | 21-Oct-13 | 24-Oct-13 | 3 |
| LL1-2008 | LL1 - ReSteel / PT Cables L1 (Above) | 7 | 7 | 21-Oct-13 | 29-Oct-13 | 0 |
| LL1-2010 | LL1 - Install Embeds L1 (Above) | 3 | 3 | 21-Oct-13 | 23-Oct-13 | 4 |
| LL1-2012 | LL1 - Pour / Finish Deck L1 (Above) | 1 | 1 | 30-Oct-13 | 30-Oct-13 | 0 |
| LL1-2014 | LL1 - Stress Tendons L1 (Above) | 1 | 1 | 05-Nov-13 | 05-Nov-13 | 0 |

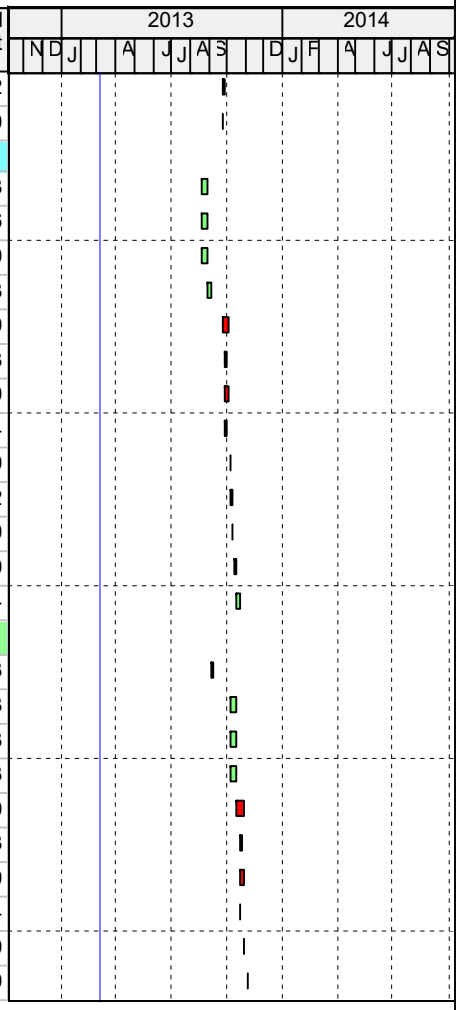



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-2016 | LL1 - Strip / ReShore Deck L1 (Above) | 3 | 3 | 06-Nov-13 | 08-Nov-13 | 0 |
| LL1-2018 | LL1 - Remove Shoring Grid Lid | 4 | 4 | 12-Nov-13 | 15-Nov-13 | 21 |
| LL1-2022 | LL1 - Waterproof City Park Deck | 3 | 3 | 12-Nov-13 | 14-Nov-13 | 29 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-2002 | L1 - FRP Columns / Misc Walls | 8 | 8 | 31-Oct-13 | 12-Nov-13 | 0 |
| L01-2000 | L1 - FRP Core Walls | 8 | 8 | 31-Oct-13 | 12-Nov-13 | 3 |
| L01-2004 | L1 - Shore / Form Deck L2 (Above) | 8 | 8 | 12-Nov-13 | 21-Nov-13 | 0 |
| L01-2006 | L1 - M & E Inserts L2 (Above) | 4 | 4 | 14-Nov-13 | 19-Nov-13 | 3 |
| L01-2008 | L1 - ReSteel / PT Cables L2 (Above) | 7 | 7 | 14-Nov-13 | 22-Nov-13 | 0 |
| L01-2010 | L1 - Install Embeds L2 (Above) | 4 | 4 | 14-Nov-13 | 19-Nov-13 | 3 |
| L01-2012 | L1 - Pour / Finish Deck L2 (Above) | 1 | 1 | 25-Nov-13 | 25-Nov-13 | 0 |
| L01-2014 | L1 - Stress Tendons L2 (Above) | 1 | 1 | 03-Dec-13 | 03-Dec-13 | 10 |
| L01-2016 | L1 - Strip / ReShore Deck L2 (Above) | 3 | 3 | 04-Dec-13 | 06-Dec-13 | 10 |
| L01-2018 | L1 - Remove Shoring Grid Lid / Grind & Patch | 2 | 2 | 09-Dec-13 | 10-Dec-13 | 10 |
| **Attic Roof** | | | | | | |
| AR-2002 | L1 - FRP Columns / Misc Walls | 4 | 4 | 13-Nov-13 | 18-Nov-13 | 0 |
| AR-2004 | L1 - Shore / Form Deck AR (Above) | 4 | 4 | 15-Nov-13 | 20-Nov-13 | 0 |
| AR-2006 | L1 - M & E Inserts AR (Above) | 2 | 2 | 19-Nov-13 | 20-Nov-13 | 2 |
| AR-2008 | L1 - ReSteel / PT Cables AR (Above) | 3 | 3 | 19-Nov-13 | 21-Nov-13 | 1 |
| AR-2010 | L1 - Install Embeds AR (Above) | 4 | 4 | 19-Nov-13 | 22-Nov-13 | 0 |
| AR-2012 | L1 - Pour / Finish Deck AR (Above) | 1 | 1 | 25-Nov-13 | 25-Nov-13 | 0 |
| AR-2014 | L1 - Stress Tendons AR (Above) | 1 | 1 | 03-Dec-13 | 03-Dec-13 | 12 |
| AR-2016 | L1 - Strip / ReShore Deck AR (Above) | 3 | 3 | 04-Dec-13 | 06-Dec-13 | 12 |
| AR-2018 | L1 - Remove Shoring Grid Lid / Grind & Patch | 2 | 2 | 09-Dec-13 | 10-Dec-13 | 12 |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-2002 | L2 - FRP Columns / Misc Walls | 5 | 5 | 26-Nov-13 | 04-Dec-13 | 0 |
| L02-2000 | L2 - FRP Core Walls | 5 | 5 | 26-Nov-13 | 04-Dec-13 | 0 |

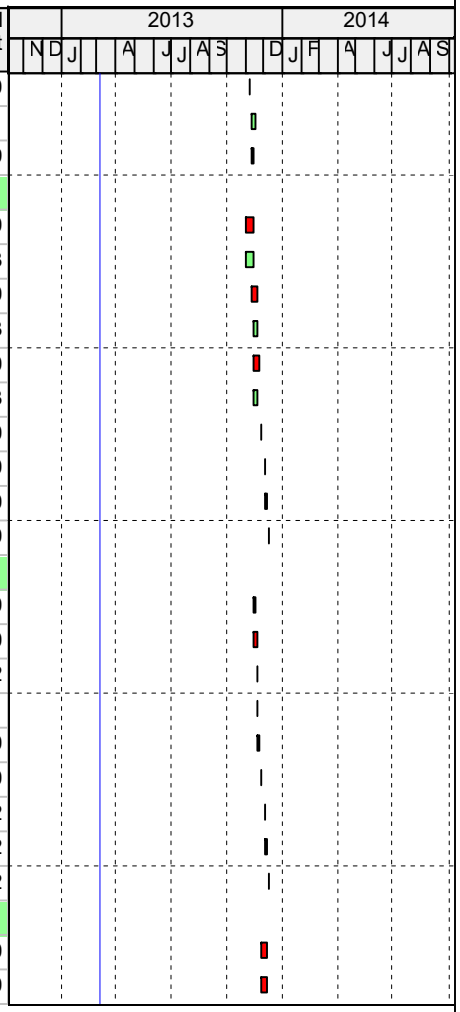



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-2004 | L2 - Shore / Form Deck L3 (Above) | 5 | 5 | 03-Dec-13 | 09-Dec-13 | 0 |
| L02-2006 | L2 - M & E Inserts L3 (Above) | 3 | 3 | 05-Dec-13 | 09-Dec-13 | 1 |
| L02-2008 | L2 - ReSteel / PT Cables L3 (Above) | 4 | 4 | 05-Dec-13 | 10-Dec-13 | 0 |
| L02-2010 | L2 - Install Embeds L3 (Above) | 4 | 4 | 05-Dec-13 | 10-Dec-13 | 0 |
| L02-2012 | L2 - Pour / Finish Deck L3 (Above) | 1 | 1 | 11-Dec-13 | 11-Dec-13 | 0 |
| L02-2014 | L2 - Stress Tendons L3 (Above) | 1 | 1 | 17-Dec-13 | 17-Dec-13 | 0 |
| L02-2016 | L2 - Strip / ReShore Deck L3 (Above) | 3 | 3 | 18-Dec-13 | 20-Dec-13 | 0 |
| L02-2018 | L2 - Remove Shoring Grid Lid / Grind & Patch | 2 | 2 | 23-Dec-13 | 24-Dec-13 | 16 |
| **Ballroom Catwalk & Roof** | | | | | | |
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 10 | 10 | 23-Dec-13 | 13-Jan-14 | 26 |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 3 | 14-Jan-14 | 16-Jan-14 | 26 |
| BR-2112 | BR - Fireproofing @ Structural Steel | 5 | 5 | 31-Jan-14 | 06-Feb-14 | 27 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool / Ballroom Roof)** | | | | | | |
| L03-2002 | L3 - FRP Columns | 2 | 2 | 12-Dec-13 | 13-Dec-13 | 4 |
| L03-2000 | L3 - FRP Core Walls | 2 | 2 | 12-Dec-13 | 13-Dec-13 | 4 |
| L03-2004 | L3 - Shore / Form Deck L4 (Above) | 2 | 2 | 16-Dec-13 | 17-Dec-13 | 4 |
| L03-2006 | L3 - M & E Inserts L4 (Above) | 1 | 1 | 17-Dec-13 | 17-Dec-13 | 5 |
| L03-2008 | L3 - ReSteel / PT Cables L4 (Above) | 2 | 2 | 17-Dec-13 | 18-Dec-13 | 4 |
| L03-2010 | L3 - Install Embeds L4 (Above) | 1 | 1 | 17-Dec-13 | 17-Dec-13 | 5 |
| L03-2012 | L3 - Pour / Finish Deck L4 (Above) | 1 | 1 | 20-Dec-13 | 20-Dec-13 | 1 |
| L03-2014 | L3 - Stress Tendons L4 (Above) | 1 | 1 | 23-Dec-13 | 23-Dec-13 | 2 |
| L03-2016 | L3 - Strip / ReShore Deck L4 (Above) | 2 | 2 | 24-Dec-13 | 30-Dec-13 | 2 |
| L03-2018 | L3 - Remove Shoring Grid Lid / Grind & Patch | 2 | 2 | 31-Dec-13 | 06-Jan-14 | 29 |
| **Level 4 - (Guest Rooms)** | | | | | | |
| L04-2002 | L4 - FRP Columns | 2 | 2 | 23-Dec-13 | 24-Dec-13 | 4 |
| L04-2000 | L4 - FRP Core Walls | 2 | 2 | 23-Dec-13 | 24-Dec-13 | 4 |

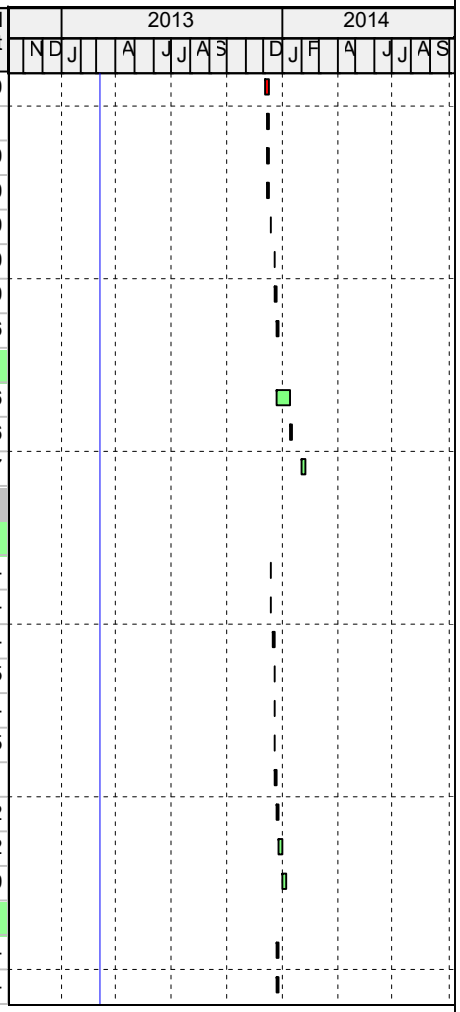



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-2004 | L4 - Shore / Form Deck L5 (Above) | 2 | 2 | 24-Dec-13 | 30-Dec-13 | 4 |
| L04-2006 | L4 - M & E Inserts L5 (Above) | 1 | 1 | 30-Dec-13 | 30-Dec-13 | 5 |
| L04-2008 | L4 - ReSteel / PT Cables L5 (Above) | 2 | 2 | 30-Dec-13 | 31-Dec-13 | 4 |
| L04-2010 | L4 - Install Embeds L5 (Above) | 1 | 1 | 30-Dec-13 | 30-Dec-13 | 5 |
| L04-2012 | L4 - Pour / Finish Deck L5 (Above) | 1 | 1 | 03-Jan-14 | 03-Jan-14 | 1 |
| L04-2014 | L4 - Stress Tendons L5 (Above) | 1 | 1 | 06-Jan-14 | 06-Jan-14 | 7 |
| L04-2016 | L4 - Strip / ReShore Deck L5 (Above) | 2 | 2 | 07-Jan-14 | 08-Jan-14 | 7 |
| L04-2018 | L4 - Remove Shoring Grid Lid / Grind & Patch | 2 | 2 | 09-Jan-14 | 10-Jan-14 | 48 |
| **Level 5 - (Guest Rooms)** | | | | | | |
| L05-2002 | L5 - FRP Columns | 2 | 2 | 06-Jan-14 | 07-Jan-14 | 10 |
| L05-2000 | L5 - FRP Core Walls | 2 | 2 | 06-Jan-14 | 07-Jan-14 | 10 |
| L05-2004 | L5 - Shore / Form Deck L6 (Above) | 2 | 2 | 07-Jan-14 | 08-Jan-14 | 10 |
| L05-2006 | L5 - M & E Inserts L6 (Above) | 1 | 1 | 08-Jan-14 | 08-Jan-14 | 11 |
| L05-2008 | L5 - ReSteel / PT Cables L6 (Above) | 2 | 2 | 08-Jan-14 | 09-Jan-14 | 10 |
| L05-2010 | L5 - Install Embeds L6 (Above) | 1 | 1 | 08-Jan-14 | 08-Jan-14 | 11 |
| L05-2012 | L5 - Pour / Finish Deck L6 (Above) | 1 | 1 | 10-Jan-14 | 10-Jan-14 | 2 |
| L05-2014 | L5 - Stress Tendons L6 (Above) | 1 | 1 | 13-Jan-14 | 13-Jan-14 | 12 |
| L05-2016 | L5 - Strip / ReShore Deck L6 (Above) | 2 | 2 | 14-Jan-14 | 15-Jan-14 | 12 |
| L05-2018 | L5 - Remove Shoring Grid Lid / Grind & Patch | 2 | 2 | 16-Jan-14 | 17-Jan-14 | 48 |
| **Level 6 - (Guest Rooms)** | | | | | | |
| L06-2002 | L6 - FRP Columns | 2 | 2 | 13-Jan-14 | 14-Jan-14 | 20 |
| L06-2000 | L6 - FRP Core Walls | 2 | 2 | 13-Jan-14 | 14-Jan-14 | 20 |
| L06-2004 | L6 - Shore / Form Deck L7 (Above) | 2 | 2 | 14-Jan-14 | 15-Jan-14 | 20 |
| L06-2006 | L6 - M & E Inserts L7 (Above) | 1 | 1 | 15-Jan-14 | 15-Jan-14 | 21 |
| L06-2008 | L6 - ReSteel / PT Cables L7 (Above) | 2 | 2 | 15-Jan-14 | 16-Jan-14 | 20 |
| L06-2010 | L6 - Install Embeds L7 (Above) | 1 | 1 | 15-Jan-14 | 15-Jan-14 | 21 |
| L06-2012 | L6 - Pour / Finish Deck L7 (Above) | 1 | 1 | 17-Jan-14 | 17-Jan-14 | 4 |

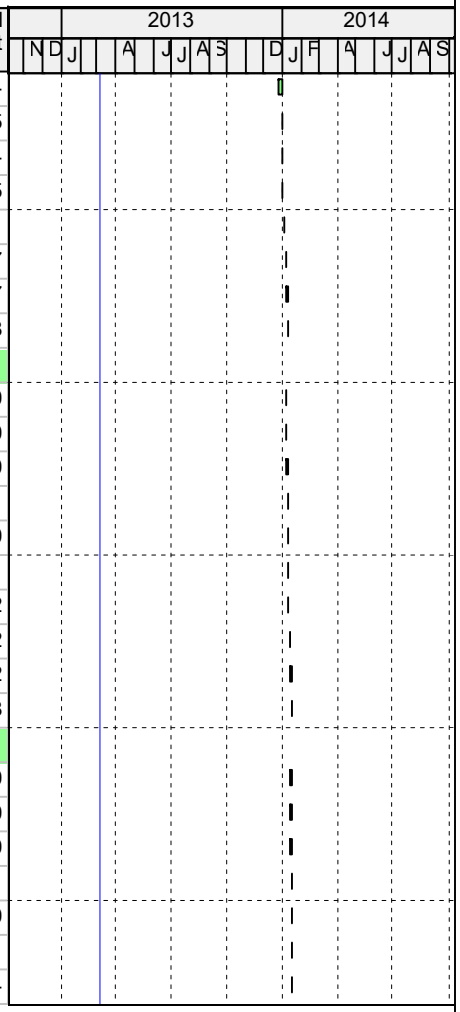



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-2014 | L6 - Stress Tendons L7 (Above) | 1 | 1 | 20-Jan-14 | 20-Jan-14 | 48 |
| L06-2016 | L6 - Strip / ReShore Deck L7 (Above) | 2 | 2 | 21-Jan-14 | 22-Jan-14 | 48 |
| L06-2018 | L6 - Remove Shoring Grid Lid / Grind & Patch | 2 | 2 | 23-Jan-14 | 24-Jan-14 | 48 |
| **Level 7 - (Guest Rooms)** | | | | | | |
| L07-2002 | L7 - FRP Columns | 2 | 2 | 20-Jan-14 | 21-Jan-14 | 20 |
| L07-2000 | L7 - FRP Core Walls | 2 | 2 | 20-Jan-14 | 21-Jan-14 | 20 |
| L07-2004 | L7 - Shore / Form Deck L8 (Above) | 2 | 2 | 21-Jan-14 | 22-Jan-14 | 20 |
| L07-2006 | L7 - M & E Inserts L8 (Above) | 1 | 1 | 22-Jan-14 | 22-Jan-14 | 21 |
| L07-2008 | L7 - ReSteel / PT Cables L8 (Above) | 2 | 2 | 22-Jan-14 | 23-Jan-14 | 20 |
| L07-2010 | L7 - Install Embeds L8 (Above) | 1 | 1 | 22-Jan-14 | 22-Jan-14 | 21 |
| L07-2012 | L7 - Pour / Finish Deck L8 (Above) | 1 | 1 | 24-Jan-14 | 24-Jan-14 | 4 |
| L07-2014 | L7 - Stress Tendons L8 (Above) | 1 | 1 | 27-Jan-14 | 27-Jan-14 | 48 |
| L07-2016 | L7 - Strip / ReShore Deck L8 (Above) | 2 | 2 | 28-Jan-14 | 29-Jan-14 | 48 |
| L07-2018 | L7 - Remove Shoring Grid Lid / Grind & Patch | 2 | 2 | 30-Jan-14 | 31-Jan-14 | 48 |
| **Level 8 - (Guest Rooms)** | | | | | | |
| L08-2002 | L8 - FRP Columns | 2 | 2 | 27-Jan-14 | 28-Jan-14 | 20 |
| L08-2000 | L8 - FRP Core Walls | 2 | 2 | 27-Jan-14 | 28-Jan-14 | 20 |
| L08-2004 | L8 - Shore / Form Deck L9 (Above) | 2 | 2 | 28-Jan-14 | 29-Jan-14 | 20 |
| L08-2006 | L8 - M & E Inserts L9 (Above) | 1 | 1 | 29-Jan-14 | 29-Jan-14 | 21 |
| L08-2008 | L8 - ReSteel / PT Cables L9 (Above) | 2 | 2 | 29-Jan-14 | 30-Jan-14 | 20 |
| L08-2010 | L8 - Install Embeds L9 (Above) | 1 | 1 | 29-Jan-14 | 29-Jan-14 | 21 |
| L08-2012 | L8 - Pour / Finish Deck L9 (Above) | 1 | 1 | 31-Jan-14 | 31-Jan-14 | 4 |
| L08-2014 | L8 - Stress Tendons L9 (Above) | 1 | 1 | 03-Feb-14 | 03-Feb-14 | 48 |
| L08-2016 | L8 - Strip / ReShore Deck L9 (Above) | 2 | 2 | 04-Feb-14 | 05-Feb-14 | 48 |
| L08-2018 | L8 - Remove Shoring Grid Lid / Grind & Patch | 2 | 2 | 06-Feb-14 | 07-Feb-14 | 48 |
| **Level 9 - (Guest Rooms)** | | | | | | |
| L09-2002 | L9 - FRP Columns | 2 | 2 | 03-Feb-14 | 04-Feb-14 | 20 |

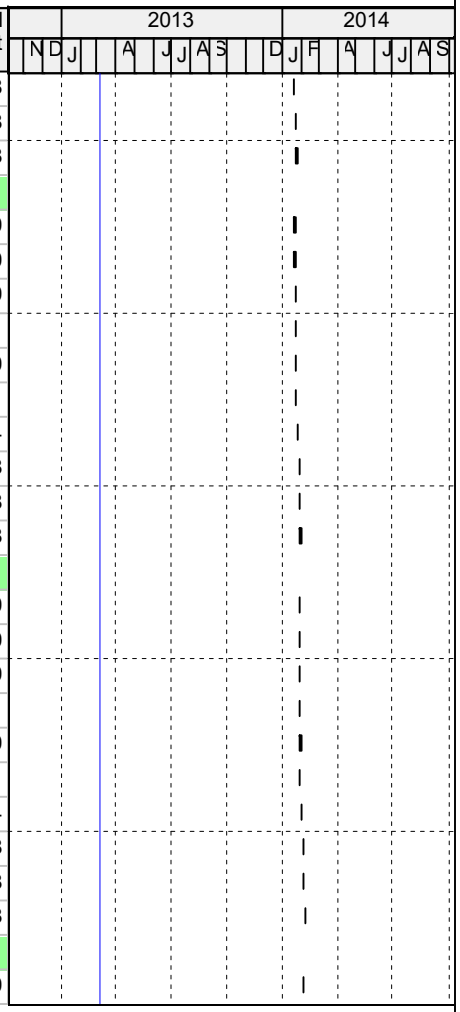



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-2000 | L9 - FRP Core Walls | 2 | 2 | 03-Feb-14 | 04-Feb-14 | 20 |
| L09-2004 | L9 - Shore / Form Deck L10 (Above) | 2 | 2 | 04-Feb-14 | 05-Feb-14 | 20 |
| L09-2006 | L9 - M & E Inserts L10 (Above) | 1 | 1 | 05-Feb-14 | 05-Feb-14 | 21 |
| L09-2008 | L9 - ReSteel / PT Cables L10 (Above) | 2 | 2 | 05-Feb-14 | 06-Feb-14 | 20 |
| L09-2010 | L9 - Install Embeds L10 (Above) | 1 | 1 | 05-Feb-14 | 05-Feb-14 | 21 |
| L09-2012 | L9 - Pour / Finish Deck L10 (Above) | 1 | 1 | 07-Feb-14 | 07-Feb-14 | 4 |
| L09-2014 | L9 - Stress Tendons L10 (Above) | 1 | 1 | 10-Feb-14 | 10-Feb-14 | 48 |
| L09-2016 | L9 - Strip / ReShore Deck L10 (Above) | 2 | 2 | 11-Feb-14 | 12-Feb-14 | 48 |
| L09-2018 | L9 - Remove Shoring Grid Lid / Grind & Patch | 2 | 2 | 13-Feb-14 | 14-Feb-14 | 48 |
| **Level 10 - (Guest Rooms)** | | | | | | |
| L10-2002 | L10 - FRP Columns | 2 | 2 | 10-Feb-14 | 11-Feb-14 | 20 |
| L10-2000 | L10 - FRP Core Walls | 2 | 2 | 10-Feb-14 | 11-Feb-14 | 20 |
| L10-2004 | L10 - Shore / Form Deck L11 (Above) | 2 | 2 | 11-Feb-14 | 12-Feb-14 | 20 |
| L10-2006 | L10 - M & E Inserts L11 (Above) | 1 | 1 | 12-Feb-14 | 12-Feb-14 | 21 |
| L10-2008 | L10 - ReSteel / PT Cables L11 (Above) | 2 | 2 | 12-Feb-14 | 13-Feb-14 | 20 |
| L10-2010 | L10 - Install Embeds L11 (Above) | 1 | 1 | 12-Feb-14 | 12-Feb-14 | 21 |
| L10-2012 | L10 - Pour / Finish Deck L11 (Above) | 1 | 1 | 14-Feb-14 | 14-Feb-14 | 4 |
| L10-2014 | L10 - Stress Tendons L11 (Above) | 1 | 1 | 17-Feb-14 | 17-Feb-14 | 48 |
| L10-2016 | L10 - Strip / ReShore Deck L11 (Above) | 2 | 2 | 18-Feb-14 | 19-Feb-14 | 48 |
| L10-2018 | L10 - Remove Shoring Grid Lid / Grind & Patch | 2 | 2 | 20-Feb-14 | 21-Feb-14 | 48 |
| **Level 11 - (Guest Rooms)** | | | | | | |
| L11-2002 | L11 - FRP Columns | 2 | 2 | 17-Feb-14 | 18-Feb-14 | 20 |
| L11-2000 | L11 - FRP Core Walls | 2 | 2 | 17-Feb-14 | 18-Feb-14 | 20 |
| L11-2004 | L11 - Shore / Form Deck L12 (Above) | 2 | 2 | 18-Feb-14 | 19-Feb-14 | 20 |
| L11-2006 | L11 - M & E Inserts L12 (Above) | 1 | 1 | 19-Feb-14 | 19-Feb-14 | 21 |
| L11-2008 | L11 - ReSteel / PT Cables L12 (Above) | 2 | 2 | 19-Feb-14 | 20-Feb-14 | 20 |
| L11-2010 | L11 - Install Embeds L12 (Above) | 1 | 1 | 19-Feb-14 | 19-Feb-14 | 21 |

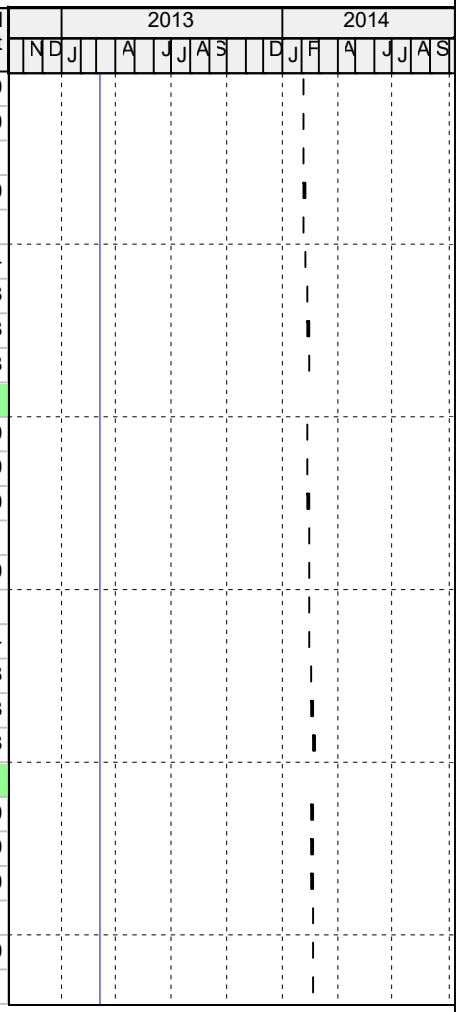



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-2012 | L11 - Pour / Finish Deck L12 (Above) | 1 | 1 | 21-Feb-14 | 21-Feb-14 | 4 |
| L11-2014 | L11 - Stress Tendons L12 (Above) | 1 | 1 | 24-Feb-14 | 24-Feb-14 | 48 |
| L11-2016 | L11 - Strip / ReShore Deck L12 (Above) | 2 | 2 | 25-Feb-14 | 26-Feb-14 | 48 |
| L11-2018 | L11 - Remove Shoring Grid Lid / Grind & Patch | 2 | 2 | 27-Feb-14 | 28-Feb-14 | 48 |
| **Level 12 - (Guest Rooms)** | | | | | | |
| L12-2002 | L12 - FRP Columns | 2 | 2 | 24-Feb-14 | 25-Feb-14 | 20 |
| L12-2000 | L12 - FRP Core Walls | 2 | 2 | 24-Feb-14 | 25-Feb-14 | 20 |
| L12-2004 | L12 - Shore / Form Deck L14 (Above) | 2 | 2 | 25-Feb-14 | 26-Feb-14 | 20 |
| L12-2006 | L12 - M & E Inserts L14 (Above) | 1 | 1 | 26-Feb-14 | 26-Feb-14 | 21 |
| L12-2008 | L12 - ReSteel / PT Cables L14 (Above) | 2 | 2 | 26-Feb-14 | 27-Feb-14 | 20 |
| L12-2010 | L12 - Install Embeds L14 (Above) | 1 | 1 | 26-Feb-14 | 26-Feb-14 | 21 |
| L12-2012 | L12 - Pour / Finish Deck L14 (Above) | 1 | 1 | 28-Feb-14 | 28-Feb-14 | 4 |
| L12-2014 | L12 - Stress Tendons L14 (Above) | 1 | 1 | 03-Mar-14 | 03-Mar-14 | 48 |
| L12-2016 | L12 - Strip / ReShore Deck L14 (Above) | 2 | 2 | 04-Mar-14 | 05-Mar-14 | 48 |
| L12-2018 | L12 - Remove Shoring Grid Lid / Grind & Patch | 2 | 2 | 06-Mar-14 | 07-Mar-14 | 48 |
| **Level 14 - (Guest Rooms)** | | | | | | |
| L14-2002 | L14 - FRP Columns | 2 | 2 | 03-Mar-14 | 04-Mar-14 | 25 |
| L14-2000 | L14 - FRP Core Walls | 2 | 2 | 03-Mar-14 | 04-Mar-14 | 25 |
| L14-2004 | L14 - Shore / Form Deck L15 (Above) | 2 | 2 | 04-Mar-14 | 05-Mar-14 | 25 |
| L14-2006 | L14 - M & E Inserts L15 (Above) | 1 | 1 | 05-Mar-14 | 05-Mar-14 | 26 |
| L14-2008 | L14 - ReSteel / PT Cables L15 (Above) | 2 | 2 | 05-Mar-14 | 06-Mar-14 | 25 |
| L14-2010 | L14 - Install Embeds L15 (Above) | 1 | 1 | 05-Mar-14 | 05-Mar-14 | 26 |
| L14-2012 | L14 - Pour / Finish Deck L15 (Above) | 1 | 1 | 07-Mar-14 | 07-Mar-14 | 5 |
| L14-2014 | L14 - Stress Tendons L15 (Above) | 1 | 1 | 10-Mar-14 | 10-Mar-14 | 48 |
| L14-2016 | L14 - Strip / ReShore Deck L15 (Above) | 2 | 2 | 11-Mar-14 | 12-Mar-14 | 48 |
| L14-2018 | L14 - Remove Shoring Grid Lid / Grind & Patch | 2 | 2 | 13-Mar-14 | 14-Mar-14 | 48 |
| **Level 15 - (Guest Rooms)** | | | | | | |

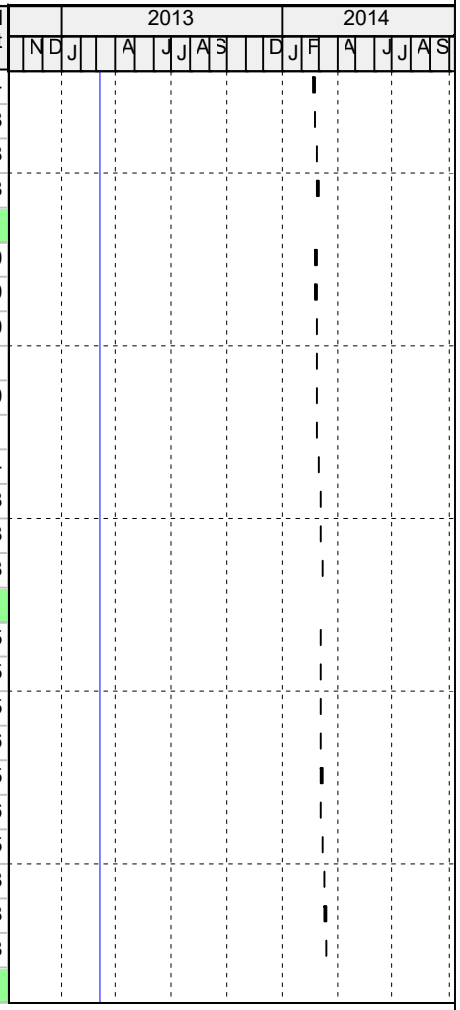



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-2002 | L15 - FRP Columns | 2 | 2 | 10-Mar-14 | 11-Mar-14 | 25 |
| L15-2000 | L15 - FRP Core Walls | 2 | 2 | 10-Mar-14 | 11-Mar-14 | 25 |
| L15-2004 | L15 - Shore / Form Deck L16 (Above) | 2 | 2 | 11-Mar-14 | 12-Mar-14 | 25 |
| L15-2006 | L15 - M & E Inserts L16 (Above) | 1 | 1 | 12-Mar-14 | 12-Mar-14 | 26 |
| L15-2008 | L15 - ReSteel / PT Cables L16 (Above) | 2 | 2 | 12-Mar-14 | 13-Mar-14 | 25 |
| L15-2010 | L15 - Install Embeds L16 (Above) | 1 | 1 | 12-Mar-14 | 12-Mar-14 | 26 |
| L15-2012 | L15 - Pour / Finish Deck L16 (Above) | 1 | 1 | 14-Mar-14 | 14-Mar-14 | 5 |
| L15-2014 | L15 - Stress Tendons L16 (Above) | 1 | 1 | 17-Mar-14 | 17-Mar-14 | 48 |
| L15-2016 | L15 - Strip / ReShore Deck L16 (Above) | 2 | 2 | 18-Mar-14 | 19-Mar-14 | 48 |
| L15-2018 | L15 - Remove Shoring Grid Lid / Grind & Patch | 2 | 2 | 20-Mar-14 | 21-Mar-14 | 48 |
| **Level 16 - (Guest Rooms)** | | | | | | |
| L16-2002 | L16 - FRP Columns | 2 | 2 | 17-Mar-14 | 18-Mar-14 | 25 |
| L16-2000 | L16 - FRP Core Walls | 2 | 2 | 17-Mar-14 | 18-Mar-14 | 25 |
| L16-2004 | L16 - Shore / Form Deck L17 (Above) | 2 | 2 | 18-Mar-14 | 19-Mar-14 | 25 |
| L16-2006 | L16 - M & E Inserts L17 (Above) | 1 | 1 | 19-Mar-14 | 19-Mar-14 | 26 |
| L16-2008 | L16 - ReSteel / PT Cables L17 (Above) | 2 | 2 | 19-Mar-14 | 20-Mar-14 | 25 |
| L16-2010 | L16 - Install Embeds L17 (Above) | 1 | 1 | 19-Mar-14 | 19-Mar-14 | 26 |
| L16-2012 | L16 - Pour / Finish Deck L17 (Above) | 1 | 1 | 21-Mar-14 | 21-Mar-14 | 5 |
| L16-2014 | L16 - Stress Tendons L17 (Above) | 1 | 1 | 24-Mar-14 | 24-Mar-14 | 48 |
| L16-2016 | L16 - Strip / ReShore Deck L17 (Above) | 2 | 2 | 25-Mar-14 | 26-Mar-14 | 48 |
| L16-2018 | L16 - Remove Shoring Grid Lid / Grind & Patch | 2 | 2 | 27-Mar-14 | 28-Mar-14 | 48 |
| **Level 17 - (Guest Rooms)** | | | | | | |
| L17-2002 | L17 - FRP Columns | 2 | 2 | 24-Mar-14 | 25-Mar-14 | 25 |
| L17-2000 | L17 - FRP Core Walls | 2 | 2 | 24-Mar-14 | 25-Mar-14 | 25 |
| L17-2004 | L17 - Shore / Form Deck Roof (Above) | 2 | 2 | 25-Mar-14 | 26-Mar-14 | 25 |
| L17-2006 | L17 - M & E Inserts Roof (Above) | 1 | 1 | 26-Mar-14 | 26-Mar-14 | 26 |
| L17-2008 | L17 - ReSteel / PT Cables Roof (Above) | 2 | 2 | 26-Mar-14 | 27-Mar-14 | 25 |

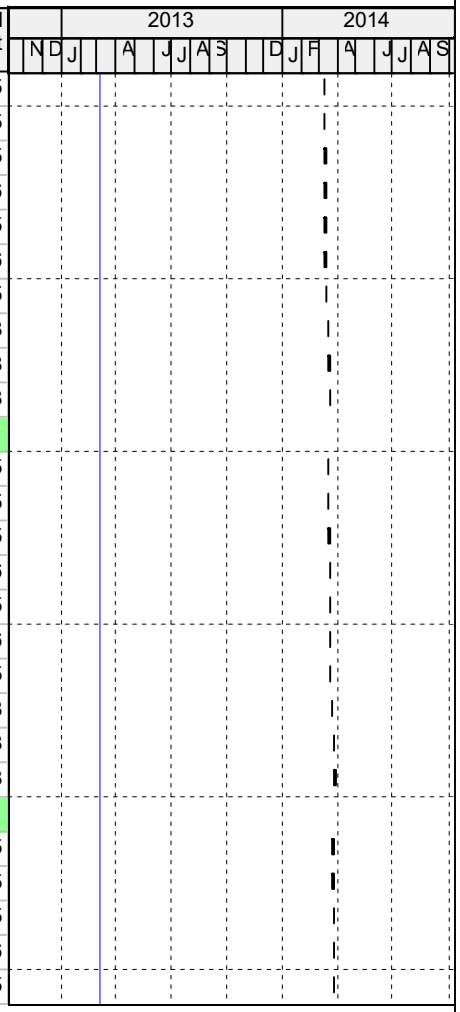



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-2010 | L17 - Install Embeds Roof (Above) | 1 | 1 | 26-Mar-14 | 26-Mar-14 | 26 |
| L17-2012 | L17 - Pour / Finish Deck Roof (Above) | 1 | 1 | 28-Mar-14 | 28-Mar-14 | 5 |
| L17-2014 | L17 - Stress Tendons Roof (Above) | 1 | 1 | 31-Mar-14 | 31-Mar-14 | 26 |
| L17-2016 | L17 - Strip / ReShore Deck Roof (Above) | 2 | 2 | 01-Apr-14 | 02-Apr-14 | 48 |
| L17-2018 | L17 - Remove Shoring Grid Lid / Grind & Patch | 2 | 2 | 03-Apr-14 | 04-Apr-14 | 48 |
| **Mech Penthouse** | | | | | | |
| PH-8700 | High Roof - Structural Steel | 10 | 10 | 01-Apr-14 | 14-Apr-14 | 91 |
| PH-8702 | PH - Structural Steel / Decking / Framing | 10 | 10 | 01-Apr-14 | 14-Apr-14 | 26 |
| PH-8704 | High Mech Roof - Structural Steel Mech Supports | 6 | 6 | 01-Apr-14 | 08-Apr-14 | 123 |
| PH-8706 | Set Mech Equipment @ Tower Roof | 2 | 2 | 09-Apr-14 | 10-Apr-14 | 123 |
| PH-8708 | Set Equipment @ Penthouse | 3 | 3 | 15-Apr-14 | 17-Apr-14 | 118 |
| **Vertical Circulation** | | | | | | |
| Stairs | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 1 | 1 | 29-Aug-13 | 29-Aug-13 | 182 |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 1 | 1 | 17-Oct-13 | 17-Oct-13 | 149 |
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 1 | 1 | 12-Nov-13 | 12-Nov-13 | 133 |
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 1 | 1 | 09-Dec-13 | 09-Dec-13 | 117 |
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 1 | 1 | 23-Dec-13 | 23-Dec-13 | 108 |
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 1 | 1 | 31-Dec-13 | 31-Dec-13 | 104 |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 1 | 1 | 09-Jan-14 | 09-Jan-14 | 99 |
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 1 | 1 | 16-Jan-14 | 16-Jan-14 | 96 |
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 1 | 1 | 23-Jan-14 | 23-Jan-14 | 92 |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 1 | 1 | 30-Jan-14 | 30-Jan-14 | 88 |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 1 | 1 | 06-Feb-14 | 06-Feb-14 | 84 |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 1 | 1 | 13-Feb-14 | 13-Feb-14 | 80 |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 1 | 1 | 20-Feb-14 | 20-Feb-14 | 76 |

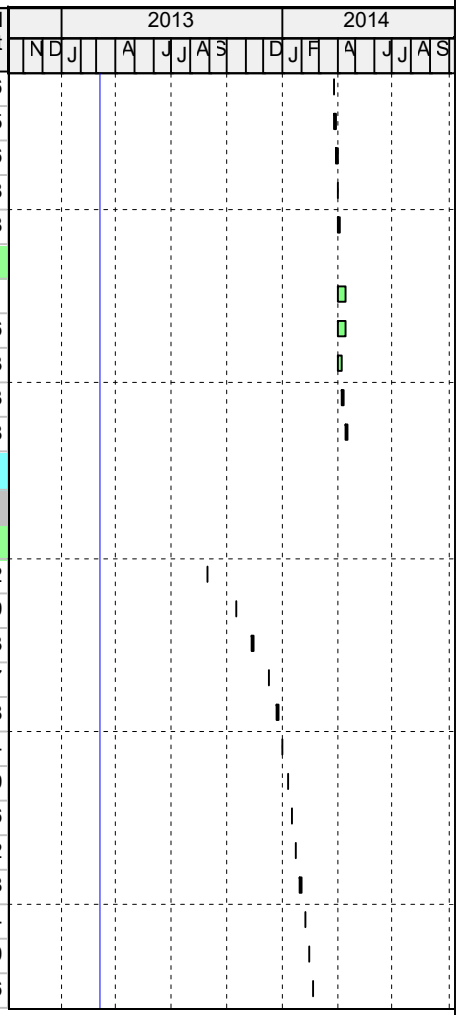



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 1 | 1 | 27-Feb-14 | 27-Feb-14 | 72 |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 1 | 1 | 06-Mar-14 | 06-Mar-14 | 68 |
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 1 | 1 | 13-Mar-14 | 13-Mar-14 | 64 |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 1 | 1 | 20-Mar-14 | 20-Mar-14 | 60 |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 1 | 1 | 27-Mar-14 | 27-Mar-14 | 56 |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 1 | 1 | 03-Apr-14 | 03-Apr-14 | 52 |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 1 | 1 | 04-Apr-14 | 04-Apr-14 | 52 |
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 1 | 1 | 29-Aug-13 | 29-Aug-13 | 178 |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 1 | 1 | 17-Oct-13 | 17-Oct-13 | 145 |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 1 | 1 | 12-Nov-13 | 12-Nov-13 | 129 |
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 1 | 1 | 09-Dec-13 | 09-Dec-13 | 113 |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 1 | 1 | 23-Dec-13 | 23-Dec-13 | 104 |
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 1 | 1 | 31-Dec-13 | 31-Dec-13 | 100 |
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 1 | 1 | 09-Jan-14 | 09-Jan-14 | 95 |
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 1 | 1 | 16-Jan-14 | 16-Jan-14 | 92 |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 1 | 1 | 23-Jan-14 | 23-Jan-14 | 88 |
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 1 | 1 | 30-Jan-14 | 30-Jan-14 | 84 |
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 1 | 1 | 06-Feb-14 | 06-Feb-14 | 80 |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 1 | 1 | 13-Feb-14 | 13-Feb-14 | 76 |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 1 | 1 | 20-Feb-14 | 20-Feb-14 | 72 |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 1 | 1 | 27-Feb-14 | 27-Feb-14 | 68 |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 1 | 1 | 06-Mar-14 | 06-Mar-14 | 64 |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 1 | 1 | 13-Mar-14 | 13-Mar-14 | 60 |
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 1 | 1 | 20-Mar-14 | 20-Mar-14 | 56 |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 1 | 1 | 27-Mar-14 | 27-Mar-14 | 52 |
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 1 | 1 | 03-Apr-14 | 03-Apr-14 | 48 |

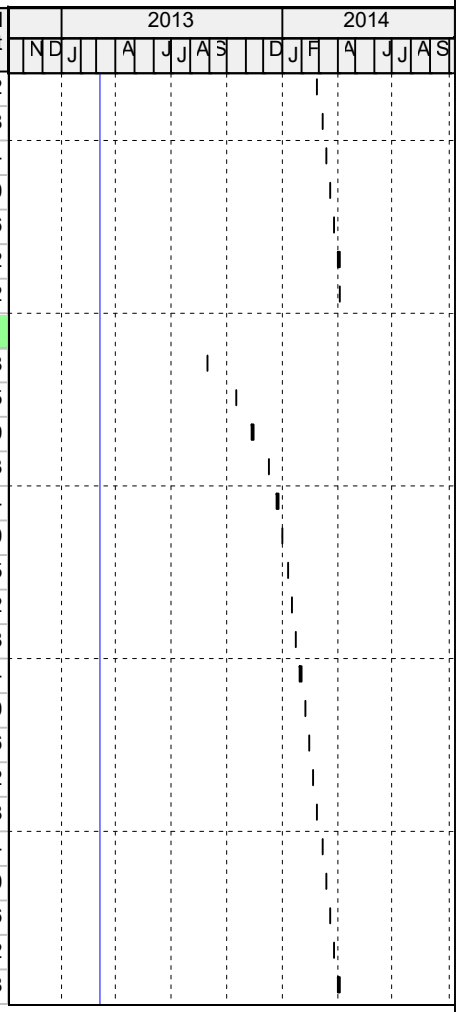



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - FRP Stairs LL2 | 6 | 6 | 08-Oct-13 | 15-Oct-13 | 52 |
| S3-4002 | Stair 3 - FRP Stairs LL1 | 6 | 6 | 31-Oct-13 | 07-Nov-13 | 41 |
| S3-4004 | Stair 3 - Permanent Railings / Final Finishes | 4 | 4 | 19-Aug-14 | 22-Aug-14 | 0 |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |
| S4-4000 | Stair 4 - FRP Stairs LL2 | 6 | 6 | 08-Oct-13 | 15-Oct-13 | 52 |
| S4-4002 | Stair 4 - FRP Stairs LL1 | 6 | 6 | 31-Oct-13 | 07-Nov-13 | 41 |
| S4-4004 | Stair 4 - FRP Stairs L1 | 6 | 6 | 26-Nov-13 | 05-Dec-13 | 34 |
| S4-4006 | Stair 4 - Permanent Railings / Final Finishes | 4 | 4 | 19-Aug-14 | 22-Aug-14 | 0 |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |
| S6-4000 | Stair 6 - FRP Stairs | 5 | 5 | 31-Oct-13 | 06-Nov-13 | 42 |
| S6-4002 | Stair 6 - Permanent Railings / Final Finishes | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 0 |
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 4 | 31-Oct-13 | 05-Nov-13 | 133 |
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 10 | 12-Nov-13 | 25-Nov-13 | 40 |
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 0 |
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a - FRP Stairs L1 | 5 | 5 | 26-Nov-13 | 04-Dec-13 | 35 |
| S4a-4002 | Stair 4a - Permanent Railings / Final Finishes | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 0 |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 17-Jun-13* | | 68 |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 49 | 17-Jun-13 | 04-Aug-13 | 99 |
| EL-1004 | Elev - Submittal Approval | 21 | 21 | 05-Aug-13 | 25-Aug-13 | 99 |
| EL-1006 | Elev - Release to Manufacturing | 14 | 14 | 10-Sep-13 | 23-Sep-13 | 84 |
| EL-1008 | Elev - Fabrication (Engineered Geared) | 120 | 120 | 24-Sep-13 | 21-Jan-14 | 84 |
| EL-1010 | Elev - Deliver to Jobsite | 1 | 1 | 22-Jan-14 | 22-Jan-14 | 60 |

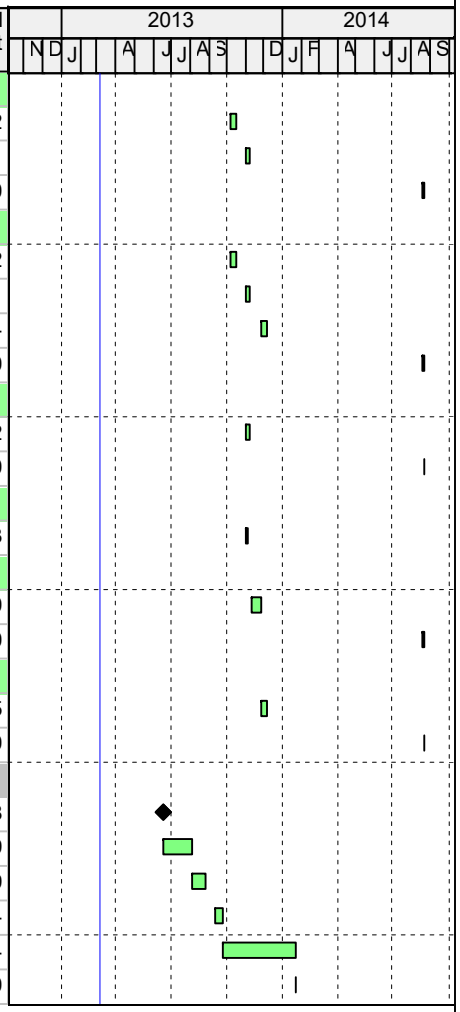



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Passenger Elevators 1-2 - LL2 to 17 - (18 Floors)** | | | | | | |
| EL-1200 | Elev 1/2 - Hoistway Clear & Ready (GC) | 0 | 0 | 07-Feb-14 | | 49 |
| EL-1202 | Elev 1/2 - Mob / Unload & Stage Equip / Materials | 5 | 5 | 07-Feb-14 | 13-Feb-14 | 49 |
| EL-1204 | Elev 1/2 - Install Rails & Brackets | 14 | 14 | 14-Feb-14 | 05-Mar-14 | 49 |
| EL-1206 | Elev 1/2 - Enclosed Mech Room w/ Power (GC) | 0 | 0 | | 08-Apr-14 | 26 |
| EL-1208 | Elev 1/2 - Install Machine & Controller | 10 | 10 | 08-Apr-14 | 21-Apr-14 | 26 |
| EL-1210 | Elev 1/2 - Install Pit Equip / Car Sling / Cwt Frame / W | 6 | 6 | 22-Apr-14 | 29-Apr-14 | 26 |
| EL-1212 | Elev 1/2 - Install Hoist & Cable | 5 | 5 | 30-Apr-14 | 06-May-14 | 26 |
| EL-1214 | Elev 1/2 - Install Entrances / Doors / Fixtures / Fascia | 15 | 15 | 07-May-14 | 28-May-14 | 26 |
| EL-1216 | Elev 1/2 - Complete Hoistway Walls (GC) | 0 | 0 | | 28-May-14 | 26 |
| EL-1218 | Elev 1/2 - Install Hoistway Equipment / Pipe & Wire | 10 | 10 | 29-May-14 | 11-Jun-14 | 26 |
| EL-1220 | Elev 1/2 - Install Cab / Wiring / Door Operators | 10 | 10 | 12-Jun-14 | 25-Jun-14 | 26 |
| EL-1222 | Elev 1/2 - Adjust | 8 | 8 | 26-Jun-14 | 08-Jul-14 | 26 |
| EL-1224 | Elev 1/2 - Clean / Paint / Punchlist | 4 | 4 | 09-Jul-14 | 14-Jul-14 | 26 |
| EL-1226 | Elev 1/2 - Inspections | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 26 |
| **Passenger Elevators 3-4 - LL4 to 17 - (20 Floors)** | | | | | | |
| EL-3400 | Elev 3/4 - Hoistway Clear & Ready (GC) | 0 | 0 | 31-Mar-14 | | 42 |
| EL-3402 | Elev 3/4 - Mob / Unload & Stage Equip / Materials | 5 | 5 | 31-Mar-14 | 04-Apr-14 | 42 |
| EL-3404 | Elev 3/4 - Install Rails & Brackets | 14 | 14 | 07-Apr-14 | 24-Apr-14 | 42 |
| EL-3406 | Elev 3/4 - Enclosed Mech Room w/ Power (GC) | 0 | 0 | | 24-Apr-14 | 42 |
| EL-3408 | Elev 3/4 - Install Machine & Controller | 10 | 10 | 25-Apr-14 | 08-May-14 | 42 |
| EL-3410 | Elev 3/4 - Install Pit Equip / Car Sling / Cwt Frame / W | 6 | 6 | 09-May-14 | 16-May-14 | 42 |
| EL-3412 | Elev 3/4 - Install Hoist & Cable | 5 | 5 | 19-May-14 | 23-May-14 | 42 |
| EL-3414 | Elev 3/4 - Install Entrances / Doors / Fixtures / Fascia | 15 | 15 | 27-May-14 | 16-Jun-14 | 42 |
| EL-3416 | Elev 3/4 - Complete Hoistway Walls (GC) | 0 | 0 | | 16-Jun-14 | 42 |
| EL-3418 | Elev 3/4 - Install Hoistway Equipment / Pipe & Wire | 10 | 10 | 17-Jun-14 | 30-Jun-14 | 42 |
| EL-3420 | Elev 3/4 - Install Cab / Wiring / Door Operators | 10 | 10 | 01-Jul-14 | 15-Jul-14 | 42 |

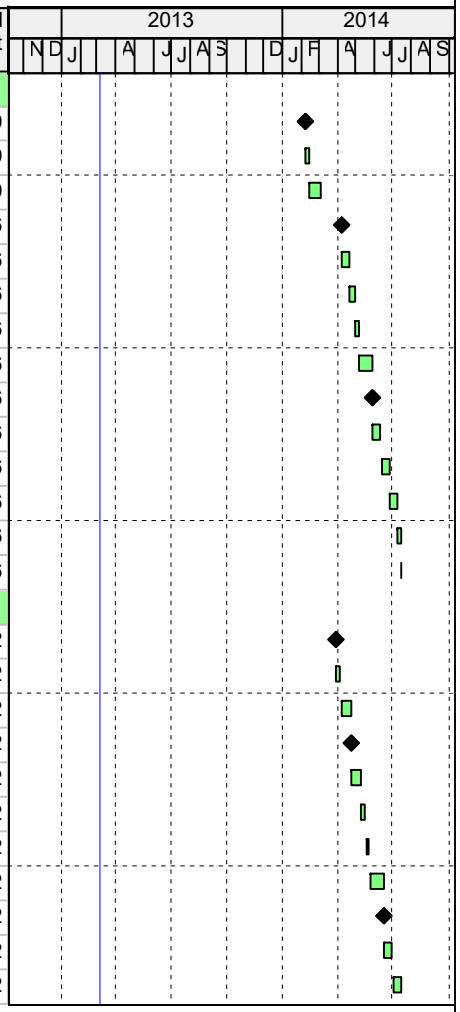



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-3422 | Elev 3/4 - Adjust | 8 | 8 | 16-Jul-14 | 25-Jul-14 | 42 |
| EL-3424 | Elev 3/4 - Clean / Paint / Punchlist | 4 | 4 | 28-Jul-14 | 31-Jul-14 | 42 |
| EL-3426 | Elev 3/4 - Inspections | 2 | 2 | 01-Aug-14 | 04-Aug-14 | 42 |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 31-Mar-14 | | 30 |
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 5 | 5 | 31-Mar-14 | 04-Apr-14 | 30 |
| EL-5004 | Elev 5 - Install Rails & Brackets | 15 | 15 | 07-Apr-14 | 25-Apr-14 | 30 |
| EL-5006 | Elev 5 - Enclosed Mech Room w/ Power (GC) | 0 | 0 | | 25-Apr-14 | 30 |
| EL-5008 | Elev 5 - Install Machine & Controller | 14 | 14 | 28-Apr-14 | 15-May-14 | 30 |
| EL-5010 | Elev 5 - Install Pit Equip / Car Sling / Cwt Frame / Wei | 8 | 8 | 16-May-14 | 28-May-14 | 30 |
| EL-5012 | Elev 5 - Install Hoist & Cable | 5 | 5 | 29-May-14 | 04-Jun-14 | 30 |
| EL-5014 | Elev 5 - Install Entrances / Doors / Fixtures / Fascia | 18 | 18 | 05-Jun-14 | 30-Jun-14 | 30 |
| EL-5016 | Elev 5 - Complete Hoistway Walls (GC) | 0 | 0 | | 30-Jun-14 | 30 |
| EL-5018 | Elev 5 - Install Hoistway Equipment / Pipe & Wire | 12 | 12 | 01-Jul-14 | 17-Jul-14 | 30 |
| EL-5020 | Elev 5 - Install Cab / Wiring / Door Operators | 10 | 10 | 18-Jul-14 | 31-Jul-14 | 30 |
| EL-5022 | Elev 5 - Adjust | 8 | 8 | 01-Aug-14 | 12-Aug-14 | 30 |
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 4 | 4 | 13-Aug-14 | 18-Aug-14 | 30 |
| EL-5026 | Elev 5 - Inspections | 2 | 2 | 19-Aug-14 | 20-Aug-14 | 30 |
| **Service Elevator 6 - LL2 to 1 - (3 Floors)** | | | | | | |
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 07-Apr-14 | | 65 |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 3 | 3 | 07-Apr-14 | 09-Apr-14 | 65 |
| EL-6004 | Elev 6 - Install Rails & Brackets | 10 | 10 | 10-Apr-14 | 23-Apr-14 | 65 |
| EL-6006 | Elev 6 - Enclosed Mech Room w/ Power (GC) | 0 | 0 | | 23-Apr-14 | 65 |
| EL-6008 | Elev 6 - Install Machine & Controller | 10 | 10 | 24-Apr-14 | 07-May-14 | 65 |
| EL-6010 | Elev 6 - Install Pit Equip / Car Sling / Cwt Frame / Wei | 5 | 5 | 08-May-14 | 14-May-14 | 65 |
| EL-6012 | Elev 6 - Install Hoist & Cable | 3 | 3 | 15-May-14 | 19-May-14 | 65 |
| EL-6014 | Elev 6 - Install Entrances / Doors / Fixtures / Fascia | 10 | 10 | 20-May-14 | 03-Jun-14 | 65 |

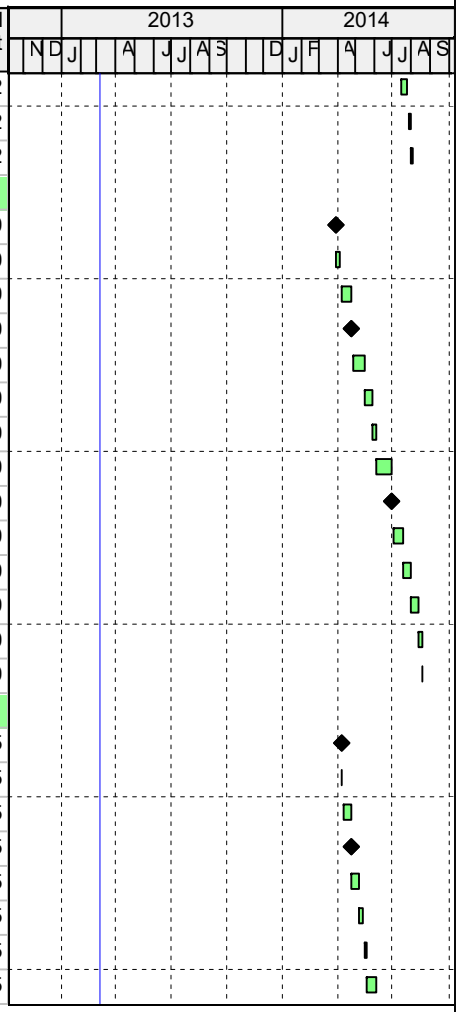



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6016 | Elev 6 - Complete Hoistway Walls (GC) | 0 | 0 | | 03-Jun-14 | 65 |
| EL-6018 | Elev 6 - Install Hoistway Equipment / Pipe & Wire | 5 | 5 | 04-Jun-14 | 10-Jun-14 | 65 |
| EL-6020 | Elev 6 - Install Cab / Wiring / Door Operators | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 65 |
| EL-6022 | Elev 6 - Adjust | 5 | 5 | 18-Jun-14 | 24-Jun-14 | 65 |
| EL-6024 | Elev 6 - Clean / Paint / Punchlist | 3 | 3 | 25-Jun-14 | 27-Jun-14 | 65 |
| EL-6026 | Elev 6 - Inspections | 2 | 2 | 30-Jun-14 | 01-Jul-14 | 65 |
| **Exterior Shell** | | | | | | |
| **Elevations** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 3** | | | | | | |
| EP-5114 | LL3 - Metal Wall Panels | 5 | 5 | 23-Dec-13 | 06-Jan-14 | 0 |
| **Lower Level 2** | | | | | | |
| EP-5116 | LL2 - Metal Wall Panels | 9 | 9 | 07-Jan-14 | 17-Jan-14 | 0 |
| **Lower Level 1** | | | | | | |
| EP-5118 | LL1 - Metal Wall Panels | 10 | 10 | 20-Jan-14 | 31-Jan-14 | 0 |
| **Level 1** | | | | | | |
| EP-5102 | L1 - Curtainwall Frames @ Entry / Lounge | 10 | 10 | 14-Jan-14 | 27-Jan-14 | 39 |
| EP-5104 | L1 - Curtainwall Glazing @ Entry / Lounge | 5 | 5 | 28-Jan-14 | 03-Feb-14 | 39 |
| EP-5108 | L1 - Metal Wall Panels | 10 | 10 | 03-Feb-14 | 14-Feb-14 | 0 |
| EP-5106 | L1 - Curtainwall Field Meassured Glazing @ Entry / L | 3 | 3 | 04-Feb-14 | 06-Feb-14 | 39 |
| EP-5120 | L1 - EFIS Wall Panels | 5 | 5 | 17-Feb-14 | 21-Feb-14 | 0 |
| EP-5100 | L1 - Windows | 5 | 5 | 24-Feb-14 | 28-Feb-14 | 23 |
| EP-5110 | L1 - Revolving Doors | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 0 |
| **Level 2** | | | | | | |
| EP-5122 | L2 - EFIS Wall Panels | 5 | 5 | 24-Feb-14 | 28-Feb-14 | 0 |
| EP-5112 | L2 - Windows | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 0 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |

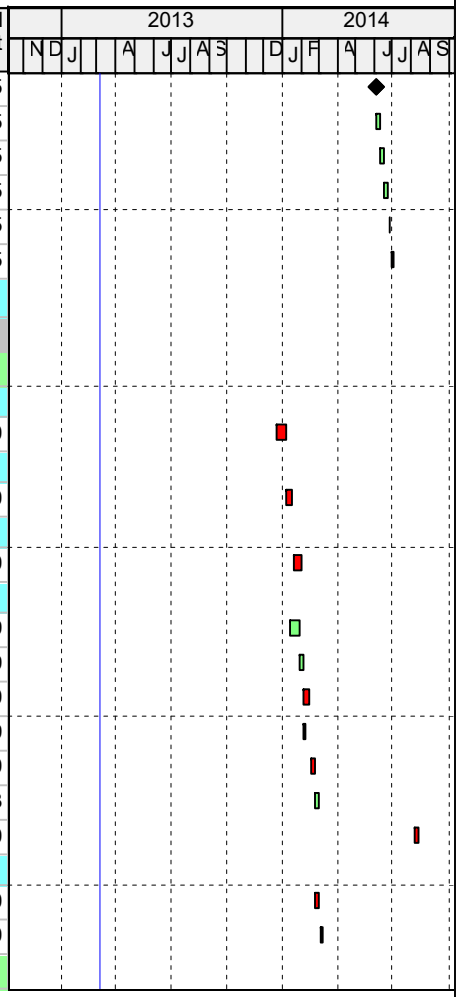



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Levels 3-4** | | | | | | |
| EP-5198 | L1 - Curtainwall Frames @ Pool | 10 | 10 | 22-Jan-14 | 04-Feb-14 | 56 |
| EP-5300 | L1 - Curtainwall Glazing @ Pool | 5 | 5 | 05-Feb-14 | 11-Feb-14 | 56 |
| EP-5302 | L1 - Curtainwall Field Messured Glazing @ Pool | 3 | 3 | 12-Feb-14 | 14-Feb-14 | 76 |
| EP-5124 | L3/4 - Erect 2 Story Vertical EIFS Wall Panels (Crane | 8 | 8 | 03-Mar-14 | 12-Mar-14 | 0 |
| EP-5126 | L3/4 - Erect Head & Sill EIFS Wall Panels (Floor Set) | 8 | 8 | 04-Mar-14 | 13-Mar-14 | 0 |
| EP-5128 | L3/4 - Plumb / Finish / Caulk EIFS Wall Panels | 8 | 8 | 05-Mar-14 | 14-Mar-14 | 0 |
| EP-5130 | L3 - Windows (Floor Set) | 5 | 5 | 10-Mar-14 | 14-Mar-14 | 0 |
| EP-5132 | L4 - Windows (Floor Set) | 5 | 5 | 17-Mar-14 | 21-Mar-14 | 0 |
| **Levels 5-6** | | | | | | |
| EP-5134 | L5/6 - Erect 2 Story Vertical EIFS Wall Panels (Crane | 8 | 8 | 17-Mar-14 | 26-Mar-14 | 0 |
| EP-5136 | L5/6 - Erect Head & Sill EIFS Wall Panels (Floor Set) | 8 | 8 | 18-Mar-14 | 27-Mar-14 | 0 |
| EP-5138 | L5/6 - Plumb / Finish / Caulk EIFS Wall Panels | 8 | 8 | 19-Mar-14 | 28-Mar-14 | 0 |
| EP-5140 | L5 - Windows (Floor Set) | 5 | 5 | 24-Mar-14 | 28-Mar-14 | 0 |
| EP-5142 | L6 - Windows (Floor Set) | 5 | 5 | 31-Mar-14 | 04-Apr-14 | 0 |
| **Levels 7-8** | | | | | | |
| EP-5144 | L7/8 - Erect 2 Story Vertical EIFS Wall Panels (Crane | 8 | 8 | 31-Mar-14 | 09-Apr-14 | 0 |
| EP-5146 | L7/8 - Erect Head & Sill EIFS Wall Panels (Floor Set) | 8 | 8 | 01-Apr-14 | 10-Apr-14 | 0 |
| EP-5148 | L7/8 - Plumb / Finish / Caulk EIFS Wall Panels | 8 | 8 | 02-Apr-14 | 11-Apr-14 | 0 |
| EP-5150 | L7 - Windows (Floor Set) | 5 | 5 | 07-Apr-14 | 11-Apr-14 | 0 |
| EP-5152 | L8 - Windows (Floor Set) | 5 | 5 | 14-Apr-14 | 18-Apr-14 | 0 |
| **Levels 9-10** | | | | | | |
| EP-5154 | L9/10 - Erect 2 Story Vertical EIFS Wall Panels (Cran | 8 | 8 | 14-Apr-14 | 23-Apr-14 | 24 |
| EP-5156 | L9/10 - Erect Head & Sill EIFS Wall Panels (Floor Set | 8 | 8 | 15-Apr-14 | 24-Apr-14 | 24 |
| EP-5158 | L9/10 - Plumb / Finish / Caulk EIFS Wall Panels | 8 | 8 | 16-Apr-14 | 25-Apr-14 | 24 |
| EP-5160 | L9 - Windows (Floor Set) | 5 | 5 | 21-Apr-14 | 25-Apr-14 | 25 |
| EP-5162 | L10 - Windows (Floor Set) | 5 | 5 | 28-Apr-14 | 02-May-14 | 25 |

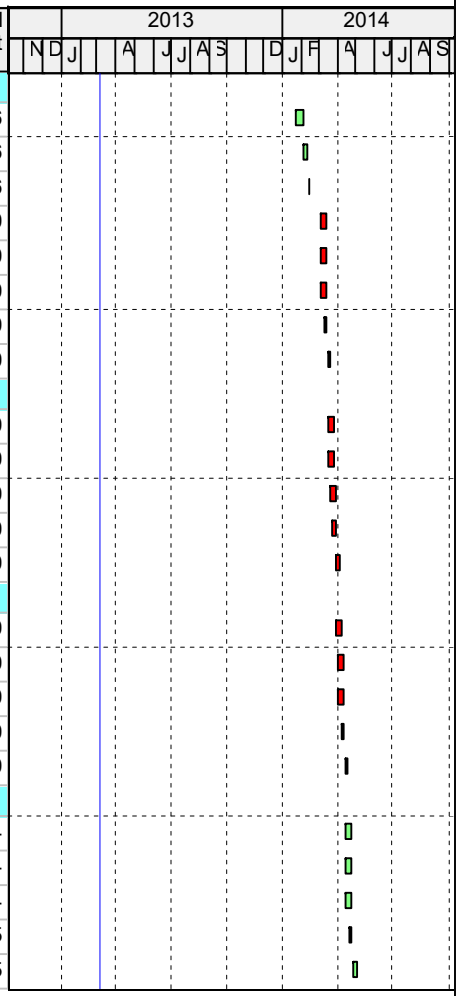



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Levels 11-12** | | | | | | |
| EP-5164 | L11/12 - Erect 2 Story Vertical EIFS Wall Panels (Crar | 8 | 8 | 28-Apr-14 | 07-May-14 | 24 |
| EP-5166 | L11/12 - Erect Head & Sill EIFS Wall Panels (Floor Se | 8 | 8 | 29-Apr-14 | 08-May-14 | 24 |
| EP-5168 | L11/12 - Plumb / Finish / Caulk EIFS Wall Panels | 8 | 8 | 30-Apr-14 | 09-May-14 | 24 |
| EP-5170 | L11 - Windows (Floor Set) | 5 | 5 | 05-May-14 | 09-May-14 | 25 |
| EP-5172 | L12 - Windows (Floor Set) | 5 | 5 | 12-May-14 | 16-May-14 | 25 |
| **Levels 14-15** | | | | | | |
| EP-5174 | L14/15 - Erect 2 Story Vertical EIFS Wall Panels (Crar | 8 | 8 | 12-May-14 | 21-May-14 | 24 |
| EP-5176 | L14/15 - Erect Head & Sill EIFS Wall Panels (Floor Se | 8 | 8 | 13-May-14 | 22-May-14 | 24 |
| EP-5178 | L14/15 - Plumb / Finish / Caulk EIFS Wall Panels | 8 | 8 | 14-May-14 | 23-May-14 | 24 |
| EP-5180 | L14 - Windows (Floor Set) | 5 | 5 | 19-May-14 | 23-May-14 | 25 |
| EP-5182 | L15 - Windows (Floor Set) | 5 | 5 | 27-May-14 | 02-Jun-14 | 25 |
| **Levels 16-17** | | | | | | |
| EP-5184 | L16/17 - Erect 2 Story Vertical EIFS Wall Panels (Crar | 8 | 8 | 27-May-14 | 05-Jun-14 | 24 |
| EP-5186 | L16/17 - Erect Head & Sill EIFS Wall Panels (Floor Se | 8 | 8 | 28-May-14 | 06-Jun-14 | 24 |
| EP-5188 | L16/17 - Plumb / Finish / Caulk EIFS Wall Panels | 8 | 8 | 29-May-14 | 09-Jun-14 | 24 |
| EP-5190 | L16 - Windows (Floor Set) | 5 | 5 | 03-Jun-14 | 09-Jun-14 | 25 |
| EP-5192 | L17 - Windows (Floor Set) | 5 | 5 | 10-Jun-14 | 16-Jun-14 | 25 |
| **Roof Level** | | | | | | |
| EP-5194 | Roof - Erect Vertical EIFS Wall Panels (Crane Set) | 6 | 6 | 10-Jun-14 | 17-Jun-14 | 24 |
| EP-5196 | Roof - Plumb / Finish / Caulk EIFS Wall Panels | 4 | 4 | 12-Jun-14 | 17-Jun-14 | 28 |
| **Mech Penthouse** | | | | | | |
| EP-5304 | PH - Erect Vertical EIFS Wall Panels (Crane Set) | 3 | 3 | 15-Apr-14 | 17-Apr-14 | 31 |
| EP-5306 | PH - Plumb / Finish / Caulk EIFS Wall Panels | 2 | 2 | 16-Apr-14 | 17-Apr-14 | 31 |
| **Hold Out Panels @ Man / Material Lifts** | | | | | | |
| EP-5200 | HoldOut - Erect 2 Story Vertical EIFS Wall Panels | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 26 |
| EP-5202 | HoldOut - Erect Head & Sill EIFS Wall Panels | 5 | 5 | 25-Jul-14 | 31-Jul-14 | 26 |
| EP-5204 | HoldOut - Plumb / Finish / Caulk EIFS Wall Panels | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 26 |

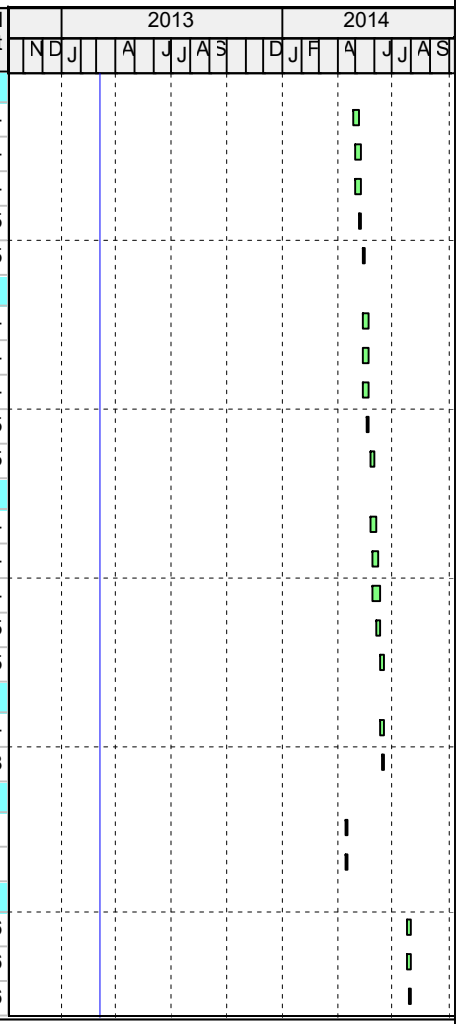



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| Roofs | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 5 | 15-Nov-13 | 21-Nov-13 | 29 |
| RF-4026 | L1 - City Park - Protection Board | 3 | 3 | 22-Nov-13 | 26-Nov-13 | 210 |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 2 | 27-Nov-13 | 02-Dec-13 | 210 |
| **Pool Membrane - (elev 18')** | | | | | | |
| RF-4034 | Pool Waterproofing / Membrane | 5 | 5 | 08-Jan-14 | 15-Jan-14 | 98 |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 15 | 15 | 11-Dec-13 | 08-Jan-14 | 23 |
| RF-4010 | AR - Set Mechanical Equipment | 5 | 5 | 09-Jan-14 | 16-Jan-14 | 22 |
| RF-4012 | AR - Coping / Flashing | 4 | 4 | 09-Jan-14 | 15-Jan-14 | 60 |
| **Entry Mechanical Roof Well - (elev 21')** | | | | | | |
| RF-4038 | Entry / Mech Well Roofing System | 5 | 5 | 22-Jan-14 | 28-Jan-14 | 28 |
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 5 | 5 | 08-Jan-14 | 15-Jan-14 | 45 |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |
| RF-4008 | RF - Entry / Porte Cochere Roofing System | 15 | 15 | 20-Jan-14 | 07-Feb-14 | 20 |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | Rf - Upper Ballroom Roofing System | 10 | 10 | 17-Jan-14 | 30-Jan-14 | 26 |
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 10 | 10 | 08-Jan-14 | 21-Jan-14 | 34 |
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |
| RF-4018 | TR - Terrace Roof - Roofing System | 5 | 5 | 11-Mar-14 | 17-Mar-14 | 67 |
| RF-4020 | TR - Terrace Roof - Coping / Flashing | 3 | 3 | 18-Mar-14 | 20-Mar-14 | 138 |
| RF-4022 | TR - Terrace Roof - Glass Railing | 5 | 5 | 18-Mar-14 | 24-Mar-14 | 107 |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Substrates / Land Mech | 20 | 20 | 10-Jun-14 | 08-Jul-14 | 24 |

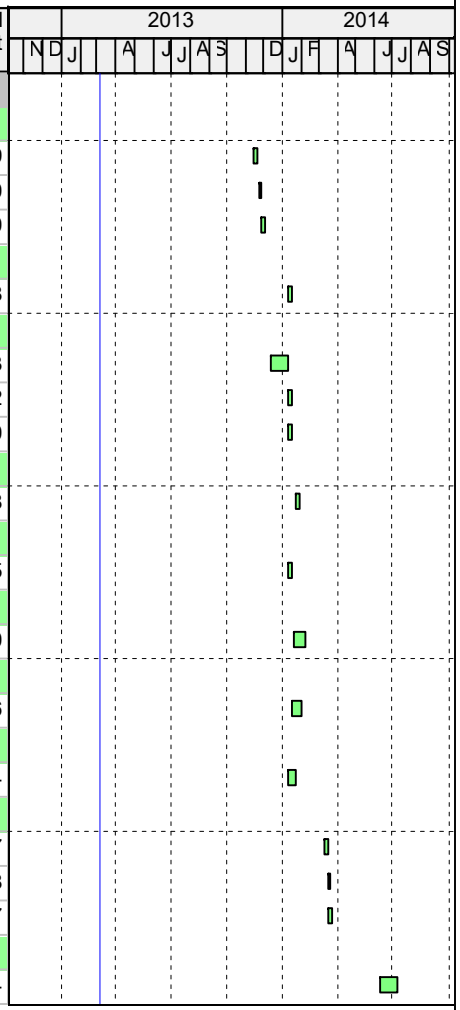



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| RF-4002 | Tower Roof - Roofing / Roof Structures | 18 | 18 | 24-Jun-14 | 18-Jul-14 | 24 |
| **PH - Roof - (elev 173')** | | | | | | |
| RF-4030 | PH - Roofing System | 5 | 5 | 18-Apr-14 | 24-Apr-14 | 31 |
| RF-4032 | PH - Coping / Flashing | 2 | 2 | 25-Apr-14 | 28-Apr-14 | 111 |
| **Rough-In's** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6000 | LL4 - Skim Ceiling | 4 | 4 | 13-Aug-13 | 16-Aug-13 | 115 |
| LL4-6002 | LL4 - Layout | 1 | 1 | 19-Aug-13 | 19-Aug-13 | 115 |
| LL4-6004 | LL4 - CMU Walls | 5 | 5 | 20-Aug-13 | 26-Aug-13 | 115 |
| LL4-6008 | LL4 - Int Wall Framing | 5 | 5 | 27-Aug-13 | 03-Sep-13 | 115 |
| LL4-6010 | LL4 - F/P Curbs | 5 | 5 | 27-Aug-13 | 03-Sep-13 | 125 |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 2 | 27-Aug-13 | 28-Aug-13 | 128 |
| LL4-6012 | LL4 - Fire Sprinkler RI | 10 | 10 | 04-Sep-13 | 17-Sep-13 | 115 |
| LL4-6014 | LL4 - Plumbing RI | 10 | 10 | 04-Sep-13 | 17-Sep-13 | 115 |
| LL4-6016 | LL4 - Electrical RI | 10 | 10 | 04-Sep-13 | 17-Sep-13 | 115 |
| LL4-6018 | LL4 - HVAC RI | 10 | 10 | 04-Sep-13 | 17-Sep-13 | 115 |
| LL4-6020 | LL4 - H Mtl Frames | 3 | 3 | 04-Sep-13 | 06-Sep-13 | 122 |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties RI | 8 | 8 | 04-Sep-13 | 13-Sep-13 | 193 |
| LL4-6024 | LL4 - Inspections | 2 | 2 | 18-Sep-13 | 19-Sep-13 | 115 |
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6000 | LL3 - Skim Ceiling | 4 | 4 | 11-Sep-13 | 16-Sep-13 | 96 |
| LL3-6002 | LL3 - Layout | 1 | 1 | 17-Sep-13 | 17-Sep-13 | 96 |
| LL3-6004 | LL3 - CMU Walls | 5 | 5 | 18-Sep-13 | 24-Sep-13 | 96 |
| LL3-6008 | LL3 - Int Wall Framing | 5 | 5 | 25-Sep-13 | 01-Oct-13 | 96 |
| LL3-6010 | LL3 - F/P Curbs | 5 | 5 | 25-Sep-13 | 01-Oct-13 | 106 |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 2 | 25-Sep-13 | 26-Sep-13 | 109 |

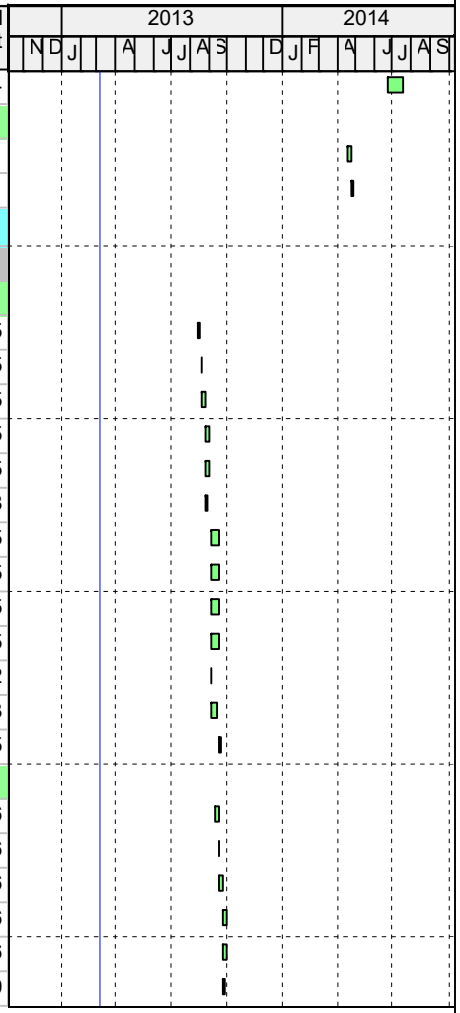



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-6012 | LL3 - Fire Sprinkler RI | 10 | 10 | 02-Oct-13 | 15-Oct-13 | 96 |
| LL3-6014 | LL3 - Plumbing RI | 10 | 10 | 02-Oct-13 | 15-Oct-13 | 96 |
| LL3-6016 | LL3 - Electrical RI | 10 | 10 | 02-Oct-13 | 15-Oct-13 | 96 |
| LL3-6018 | LL3 - HVAC RI | 10 | 10 | 02-Oct-13 | 15-Oct-13 | 96 |
| LL3-6020 | LL3 - H Mtl Frames | 3 | 3 | 02-Oct-13 | 04-Oct-13 | 103 |
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties RI | 8 | 8 | 02-Oct-13 | 11-Oct-13 | 178 |
| LL3-6024 | LL3 - Inspections | 2 | 2 | 16-Oct-13 | 17-Oct-13 | 96 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6000 | LL2 - Skim Ceiling | 4 | 4 | 23-Oct-13 | 28-Oct-13 | 54 |
| LL2-6002 | LL2 - Layout | 1 | 1 | 29-Oct-13 | 29-Oct-13 | 54 |
| LL2-6004 | LL2 - CMU Walls | 18 | 18 | 30-Oct-13 | 25-Nov-13 | 54 |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 3 | 30-Oct-13 | 01-Nov-13 | 67 |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 2 | 2 | 04-Nov-13 | 05-Nov-13 | 67 |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 5 | 26-Nov-13 | 04-Dec-13 | 54 |
| LL2-6010 | LL2 - F/P Curbs @ Parking | 5 | 5 | 26-Nov-13 | 04-Dec-13 | 160 |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 4 | 26-Nov-13 | 03-Dec-13 | 65 |
| LL2-6012 | LL2 - Fire Sprinkler RI | 10 | 10 | 05-Dec-13 | 18-Dec-13 | 54 |
| LL2-6014 | LL2 - Plumbing RI | 10 | 10 | 05-Dec-13 | 18-Dec-13 | 54 |
| LL2-6016 | LL2 - Electrical RI | 10 | 10 | 05-Dec-13 | 18-Dec-13 | 54 |
| LL2-6018 | LL2 - HVAC RI | 10 | 10 | 05-Dec-13 | 18-Dec-13 | 54 |
| LL2-6020 | LL2 - H Mtl Frames | 3 | 3 | 05-Dec-13 | 09-Dec-13 | 61 |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties RI | 8 | 8 | 05-Dec-13 | 16-Dec-13 | 129 |
| LL2-6024 | LL2 - Inspections | 2 | 2 | 19-Dec-13 | 20-Dec-13 | 54 |
| LL2-6015 | LL2 - Main Elect Room Set Equip / RI - Power to Ma | 40 | 40 | 12-Feb-14 | 08-Apr-14 | 56 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6000 | LL1 - Skim Ceiling | 5 | 5 | 18-Nov-13 | 22-Nov-13 | 21 |

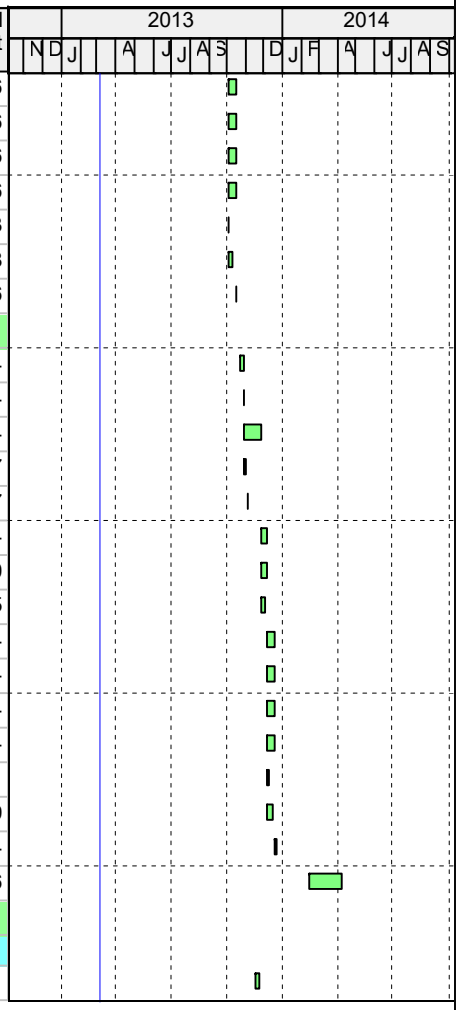



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-6002 | LL1 - Layout | 1 | 1 | 25-Nov-13 | 25-Nov-13 | 21 |
| LL1-6004 | LL1 - CMU Walls | 9 | 9 | 26-Nov-13 | 10-Dec-13 | 21 |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 3 | 26-Nov-13 | 02-Dec-13 | 24 |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 3 | 3 | 03-Dec-13 | 05-Dec-13 | 24 |
| LL1-6008 | LL1 - Int Wall Framing | 15 | 15 | 11-Dec-13 | 02-Jan-14 | 21 |
| LL1-6010 | LL1 - CMU Seismic Clips | 2 | 2 | 11-Dec-13 | 12-Dec-13 | 64 |
| LL1-6012 | LL1 - Fire Sprinkler RI | 14 | 14 | 03-Jan-14 | 23-Jan-14 | 37 |
| LL1-6014 | LL1 - Plumbing RI | 15 | 15 | 03-Jan-14 | 24-Jan-14 | 36 |
| LL1-6016 | LL1 - Electrical RI | 25 | 25 | 03-Jan-14 | 07-Feb-14 | 26 |
| LL1-6018 | LL1 - HVAC RI | 30 | 30 | 03-Jan-14 | 14-Feb-14 | 21 |
| LL1-6020 | LL1 - H Mtl Frames | 5 | 5 | 03-Jan-14 | 09-Jan-14 | 46 |
| LL1-6022 | LL1 - Fire Alarm / Elec Specialties RI | 10 | 10 | 03-Jan-14 | 17-Jan-14 | 85 |
| LL1-6024 | LL1 - Inspections | 2 | 2 | 17-Feb-14 | 18-Feb-14 | 21 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-6000 | L1 - Skim Ceiling | 5 | 5 | 11-Dec-13 | 17-Dec-13 | 10 |
| L01-6002 | L1 - Layout | 1 | 1 | 18-Dec-13 | 18-Dec-13 | 10 |
| L01-6004 | L1 - CMU Walls | 8 | 8 | 19-Dec-13 | 31-Dec-13 | 17 |
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 5 | 19-Dec-13 | 26-Dec-13 | 10 |
| L01-6006 | L1 - Ext Wall Framing - (Cold Formed) | 10 | 10 | 27-Dec-13 | 10-Jan-14 | 10 |
| L01-6010 | L1 - CMU Seismic Clips | 1 | 1 | 02-Jan-14 | 02-Jan-14 | 61 |
| L01-6008 | L1 - Int Wall Framing | 15 | 15 | 14-Jan-14 | 03-Feb-14 | 10 |
| L01-6012 | L1 - Fire Sprinkler RI | 14 | 14 | 04-Feb-14 | 21-Feb-14 | 26 |
| L01-6014 | L1 - Plumbing RI | 20 | 20 | 04-Feb-14 | 03-Mar-14 | 20 |
| L01-6016 | L1 - Electrical RI | 25 | 25 | 04-Feb-14 | 10-Mar-14 | 15 |
| L01-6018 | L1 - HVAC RI | 30 | 30 | 04-Feb-14 | 17-Mar-14 | 10 |
| L01-6020 | L1 - H Mtl Frames | 5 | 5 | 04-Feb-14 | 10-Feb-14 | 35 |
| L01-6022 | L1 - Fire Alarm / Elec Specialties RI | 10 | 10 | 04-Feb-14 | 17-Feb-14 | 66 |

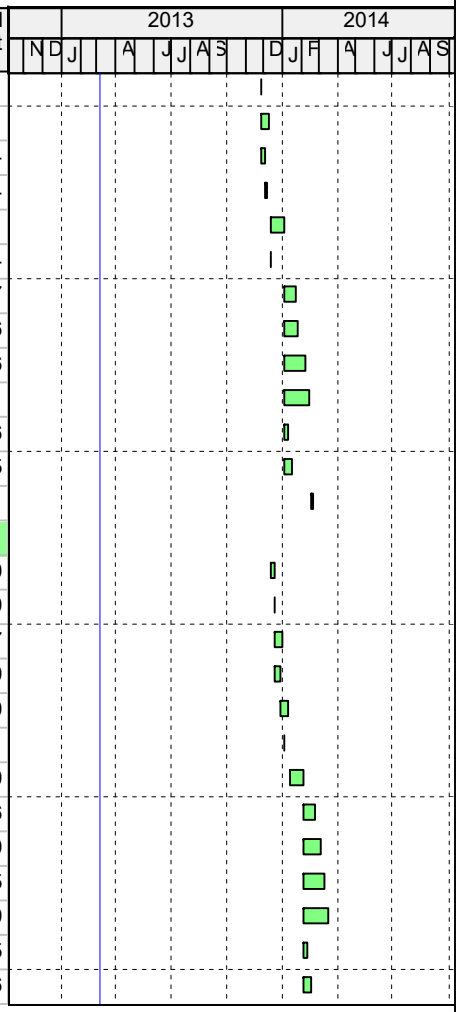



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L01-6024 | L1 - Inspections | 2 | 2 | 18-Mar-14 | 19-Mar-14 | 10 |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6000 | L2 - Grind & Patch Lid (Above) | 5 | 5 | 26-Dec-13 | 02-Jan-14 | 19 |
| L02-6002 | L2 - Layout | 1 | 1 | 03-Jan-14 | 03-Jan-14 | 19 |
| L02-6004 | L2 - CMU Walls | 5 | 5 | 06-Jan-14 | 10-Jan-14 | 33 |
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 5 | 06-Jan-14 | 10-Jan-14 | 19 |
| L02-6006 | L2 - Ext Wall Framing - (Cold Formed) | 10 | 10 | 14-Jan-14 | 27-Jan-14 | 19 |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 1 | 14-Jan-14 | 14-Jan-14 | 69 |
| L02-6008 | L2 - Int Wall Framing | 12 | 12 | 28-Jan-14 | 12-Feb-14 | 23 |
| L02-6012 | L2 - Fire Sprinkler RI | 10 | 10 | 13-Feb-14 | 26-Feb-14 | 38 |
| L02-6014 | L2 - Plumbing RI | 12 | 12 | 13-Feb-14 | 28-Feb-14 | 36 |
| L02-6016 | L2 - Electrical RI | 20 | 20 | 13-Feb-14 | 12-Mar-14 | 28 |
| L02-6018 | L2 - HVAC RI | 25 | 25 | 13-Feb-14 | 19-Mar-14 | 23 |
| L02-6020 | L2 - H Mtl Frames | 5 | 5 | 13-Feb-14 | 19-Feb-14 | 35 |
| L02-6022 | L2 - Fire Alarm / Elec Specialties RI | 10 | 10 | 13-Feb-14 | 26-Feb-14 | 63 |
| L02-6024 | L2 - Inspections | 2 | 2 | 20-Mar-14 | 21-Mar-14 | 23 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L03-6000 | L3 - Grind & Patch Lid (Above) | 4 | 4 | 07-Jan-14 | 10-Jan-14 | 46 |
| L03-6002 | L3 - Layout | 1 | 1 | 14-Jan-14 | 14-Jan-14 | 46 |
| L03-6004 | L3 - CMU Walls | 5 | 5 | 15-Jan-14 | 21-Jan-14 | 46 |
| L03-6008 | L3 - Int Wall Framing | 5 | 5 | 22-Jan-14 | 28-Jan-14 | 46 |
| L03-6010 | L3 - CMU Seismic Clips | 1 | 1 | 22-Jan-14 | 22-Jan-14 | 60 |
| L03-6012 | L3 - Fire Sprinkler RI | 10 | 10 | 29-Jan-14 | 11-Feb-14 | 46 |
| L03-6014 | L3 - Plumbing RI | 10 | 10 | 29-Jan-14 | 11-Feb-14 | 46 |
| L03-6016 | L3 - Electrical RI | 10 | 10 | 29-Jan-14 | 11-Feb-14 | 46 |
| L03-6018 | L3 - HVAC RI | 10 | 10 | 29-Jan-14 | 11-Feb-14 | 46 |

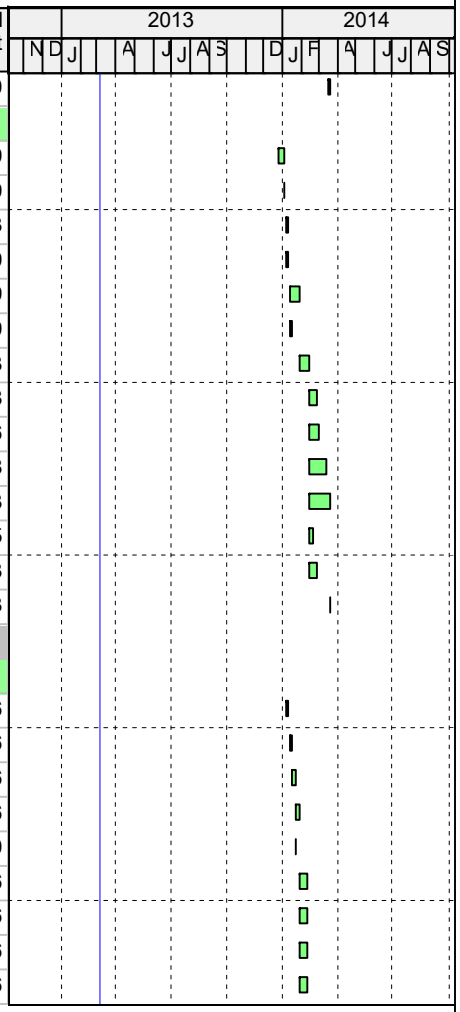



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6020 | L3 - H Mtl Frames | 3 | 3 | 29-Jan-14 | 31-Jan-14 | 58 |
| L03-6022 | L3 - Fire Alarm / Elec Specialties RI | 8 | 8 | 29-Jan-14 | 07-Feb-14 | 73 |
| L03-6024 | L3 - Inspections | 2 | 2 | 12-Feb-14 | 13-Feb-14 | 46 |
| **Level 4 - (Guest Rooms)** | | | | | | |
| L04-6000 | L4 - Grind & Patch Lid (Above) | 4 | 4 | 14-Jan-14 | 17-Jan-14 | 47 |
| L04-6002 | L4 - Layout | 1 | 1 | 20-Jan-14 | 20-Jan-14 | 47 |
| L04-6004 | L4 - CMU Walls | 5 | 5 | 21-Jan-14 | 27-Jan-14 | 47 |
| L04-6008 | L4 - Int Wall Framing | 5 | 5 | 28-Jan-14 | 03-Feb-14 | 47 |
| L04-6010 | L4 - CMU Seismic Clips | 1 | 1 | 28-Jan-14 | 28-Jan-14 | 61 |
| L04-6012 | L4 - Fire Sprinkler RI | 10 | 10 | 04-Feb-14 | 17-Feb-14 | 47 |
| L04-6014 | L4 - Plumbing RI | 10 | 10 | 04-Feb-14 | 17-Feb-14 | 47 |
| L04-6016 | L4 - Electrical RI | 10 | 10 | 04-Feb-14 | 17-Feb-14 | 47 |
| L04-6018 | L4 - HVAC RI | 10 | 10 | 04-Feb-14 | 17-Feb-14 | 47 |
| L04-6020 | L4 - H Mtl Frames | 3 | 3 | 04-Feb-14 | 06-Feb-14 | 59 |
| L04-6022 | L4 - Fire Alarm / Elec Specialties RI | 8 | 8 | 04-Feb-14 | 13-Feb-14 | 74 |
| L04-6024 | L4 - Inspections | 2 | 2 | 18-Feb-14 | 19-Feb-14 | 47 |
| **Level 5 - (Guest Rooms)** | | | | | | |
| L05-6000 | L5 - Grind & Patch Lid (Above) | 4 | 4 | 20-Jan-14 | 23-Jan-14 | 48 |
| L05-6002 | L5 - Layout | 1 | 1 | 24-Jan-14 | 24-Jan-14 | 48 |
| L05-6004 | L5 - CMU Walls | 5 | 5 | 27-Jan-14 | 31-Jan-14 | 48 |
| L05-6008 | L5 - Int Wall Framing | 5 | 5 | 03-Feb-14 | 07-Feb-14 | 48 |
| L05-6010 | L5 - CMU Seismic Clips | 1 | 1 | 03-Feb-14 | 03-Feb-14 | 62 |
| L05-6012 | L5 - Fire Sprinkler RI | 10 | 10 | 10-Feb-14 | 21-Feb-14 | 48 |
| L05-6014 | L5 - Plumbing RI | 10 | 10 | 10-Feb-14 | 21-Feb-14 | 48 |
| L05-6016 | L5 - Electrical RI | 10 | 10 | 10-Feb-14 | 21-Feb-14 | 48 |
| L05-6018 | L5 - HVAC RI | 10 | 10 | 10-Feb-14 | 21-Feb-14 | 48 |
| L05-6020 | L5 - H Mtl Frames | 3 | 3 | 10-Feb-14 | 12-Feb-14 | 60 |

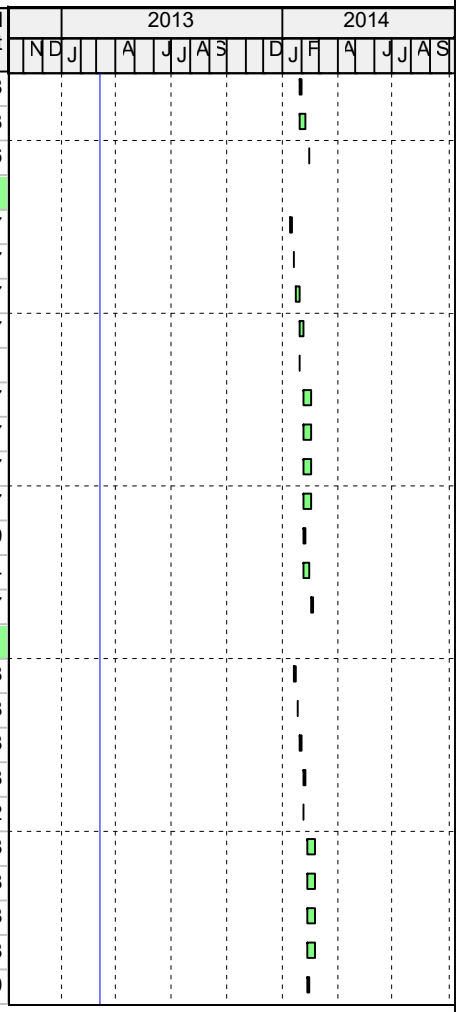



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6022 | L5 - Fire Alarm / Elec Specialties Rl | 8 | 8 | 10-Feb-14 | 19-Feb-14 | 75 |
| L05-6024 | L5 - Inspections | 2 | 2 | 24-Feb-14 | 25-Feb-14 | 48 |
| **Level 6 - (Guest Rooms)** | | | | | | |
| L06-6000 | L6 - Grind & Patch Lid (Above) | 4 | 4 | 27-Jan-14 | 30-Jan-14 | 48 |
| L06-6002 | L6 - Layout | 1 | 1 | 31-Jan-14 | 31-Jan-14 | 48 |
| L06-6004 | L6 - CMU Walls | 5 | 5 | 03-Feb-14 | 07-Feb-14 | 48 |
| L06-6008 | L6 - Int Wall Framing | 5 | 5 | 10-Feb-14 | 14-Feb-14 | 48 |
| L06-6010 | L6 - CMU Seismic Clips | 1 | 1 | 10-Feb-14 | 10-Feb-14 | 62 |
| L06-6012 | L6 - Fire Sprinkler Rl | 10 | 10 | 17-Feb-14 | 28-Feb-14 | 48 |
| L06-6014 | L6 - Plumbing Rl | 10 | 10 | 17-Feb-14 | 28-Feb-14 | 48 |
| L06-6016 | L6 - Electrical Rl | 10 | 10 | 17-Feb-14 | 28-Feb-14 | 48 |
| L06-6018 | L6 - HVAC Rl | 10 | 10 | 17-Feb-14 | 28-Feb-14 | 48 |
| L06-6020 | L6 - H Mtl Frames | 3 | 3 | 17-Feb-14 | 19-Feb-14 | 60 |
| L06-6022 | L6 - Fire Alarm / Elec Specialties Rl | 8 | 8 | 17-Feb-14 | 26-Feb-14 | 75 |
| L06-6024 | L6 - Inspections | 2 | 2 | 03-Mar-14 | 04-Mar-14 | 48 |
| **Level 7 - (Guest Rooms)** | | | | | | |
| L07-6000 | L7 - Grind & Patch Lid (Above) | 4 | 4 | 03-Feb-14 | 06-Feb-14 | 48 |
| L07-6002 | L7 - Layout | 1 | 1 | 07-Feb-14 | 07-Feb-14 | 48 |
| L07-6004 | L7 - CMU Walls | 5 | 5 | 10-Feb-14 | 14-Feb-14 | 48 |
| L07-6008 | L7 - Int Wall Framing | 5 | 5 | 17-Feb-14 | 21-Feb-14 | 48 |
| L07-6010 | L7 - CMU Seismic Clips | 1 | 1 | 17-Feb-14 | 17-Feb-14 | 62 |
| L07-6012 | L7 - Fire Sprinkler Rl | 10 | 10 | 24-Feb-14 | 07-Mar-14 | 48 |
| L07-6014 | L7 - Plumbing Rl | 10 | 10 | 24-Feb-14 | 07-Mar-14 | 48 |
| L07-6016 | L7 - Electrical Rl | 10 | 10 | 24-Feb-14 | 07-Mar-14 | 48 |
| L07-6018 | L7 - HVAC Rl | 10 | 10 | 24-Feb-14 | 07-Mar-14 | 48 |
| L07-6020 | L7 - H Mtl Frames | 3 | 3 | 24-Feb-14 | 26-Feb-14 | 60 |
| L07-6022 | L7 - Fire Alarm / Elec Specialties Rl | 8 | 8 | 24-Feb-14 | 05-Mar-14 | 75 |

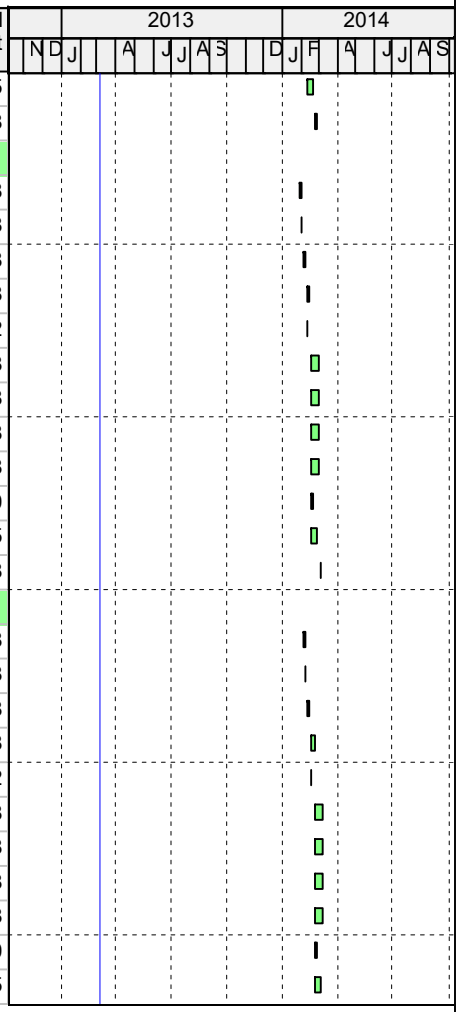



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6024 | L7 - Inspections | 2 | 2 | 10-Mar-14 | 11-Mar-14 | 48 |
| **Level 8 - (Guest Rooms)** | | | | | | |
| L08-6000 | L8 - Grind & Patch Lid (Above) | 4 | 4 | 10-Feb-14 | 13-Feb-14 | 48 |
| L08-6002 | L8 - Layout | 1 | 1 | 14-Feb-14 | 14-Feb-14 | 48 |
| L08-6004 | L8 - CMU Walls | 5 | 5 | 17-Feb-14 | 21-Feb-14 | 48 |
| L08-6008 | L8 - Int Wall Framing | 5 | 5 | 24-Feb-14 | 28-Feb-14 | 48 |
| L08-6010 | L8 - CMU Seismic Clips | 1 | 1 | 24-Feb-14 | 24-Feb-14 | 62 |
| L08-6012 | L8 - Fire Sprinkler RI | 10 | 10 | 03-Mar-14 | 14-Mar-14 | 48 |
| L08-6014 | L8 - Plumbing RI | 10 | 10 | 03-Mar-14 | 14-Mar-14 | 48 |
| L08-6016 | L8 - Electrical RI | 10 | 10 | 03-Mar-14 | 14-Mar-14 | 48 |
| L08-6018 | L8 - HVAC RI | 10 | 10 | 03-Mar-14 | 14-Mar-14 | 48 |
| L08-6020 | L8 - H Mtl Frames | 3 | 3 | 03-Mar-14 | 05-Mar-14 | 60 |
| L08-6022 | L8 - Fire Alarm / Elec Specialties RI | 8 | 8 | 03-Mar-14 | 12-Mar-14 | 75 |
| L08-6024 | L8 - Inspections | 2 | 2 | 17-Mar-14 | 18-Mar-14 | 48 |
| **Level 9 - (Guest Rooms)** | | | | | | |
| L09-6000 | L9 - Grind & Patch Lid (Above) | 4 | 4 | 17-Feb-14 | 20-Feb-14 | 48 |
| L09-6002 | L9 - Layout | 1 | 1 | 21-Feb-14 | 21-Feb-14 | 48 |
| L09-6004 | L9 - CMU Walls | 5 | 5 | 24-Feb-14 | 28-Feb-14 | 48 |
| L09-6008 | L9 - Int Wall Framing | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 48 |
| L09-6010 | L9 - CMU Seismic Clips | 1 | 1 | 03-Mar-14 | 03-Mar-14 | 62 |
| L09-6012 | L9 - Fire Sprinkler RI | 10 | 10 | 10-Mar-14 | 21-Mar-14 | 48 |
| L09-6014 | L9 - Plumbing RI | 10 | 10 | 10-Mar-14 | 21-Mar-14 | 48 |
| L09-6016 | L9 - Electrical RI | 10 | 10 | 10-Mar-14 | 21-Mar-14 | 48 |
| L09-6018 | L9 - HVAC RI | 10 | 10 | 10-Mar-14 | 21-Mar-14 | 48 |
| L09-6020 | L9 - H Mtl Frames | 3 | 3 | 10-Mar-14 | 12-Mar-14 | 60 |
| L09-6022 | L9 - Fire Alarm / Elec Specialties RI | 8 | 8 | 10-Mar-14 | 19-Mar-14 | 75 |
| L09-6024 | L9 - Inspections | 2 | 2 | 24-Mar-14 | 25-Mar-14 | 48 |

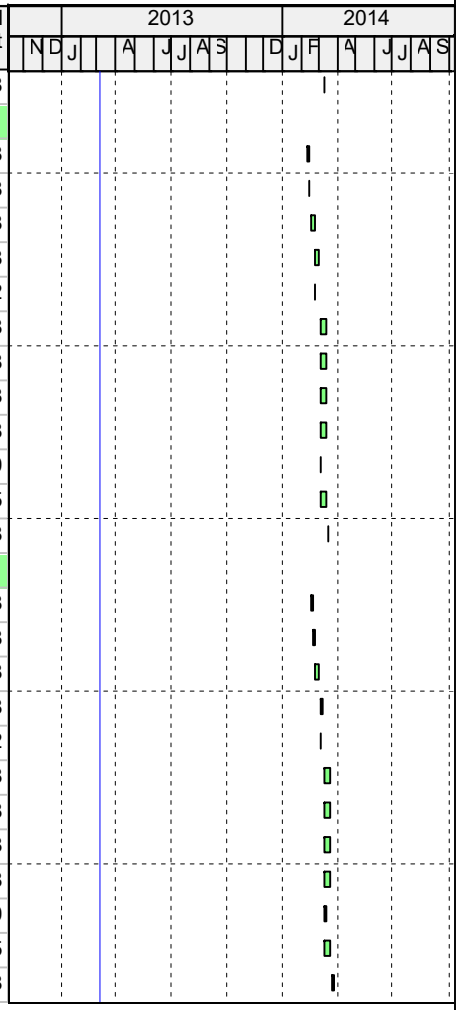



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Level 10 - (Guest Rooms)** | | | | | | |
| L10-6000 | L10 - Grind & Patch Lid (Above) | 4 | 4 | 24-Feb-14 | 27-Feb-14 | 48 |
| L10-6002 | L10 - Layout | 1 | 1 | 28-Feb-14 | 28-Feb-14 | 48 |
| L10-6004 | L10 - CMU Walls | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 48 |
| L10-6008 | L10 - Int Wall Framing | 5 | 5 | 10-Mar-14 | 14-Mar-14 | 48 |
| L10-6010 | L10 - CMU Seismic Clips | 1 | 1 | 10-Mar-14 | 10-Mar-14 | 62 |
| L10-6012 | L10 - Fire Sprinkler RI | 10 | 10 | 17-Mar-14 | 28-Mar-14 | 48 |
| L10-6014 | L10 - Plumbing RI | 10 | 10 | 17-Mar-14 | 28-Mar-14 | 48 |
| L10-6016 | L10 - Electrical RI | 10 | 10 | 17-Mar-14 | 28-Mar-14 | 48 |
| L10-6018 | L10 - HVAC RI | 10 | 10 | 17-Mar-14 | 28-Mar-14 | 48 |
| L10-6020 | L10 - H Mtl Frames | 3 | 3 | 17-Mar-14 | 19-Mar-14 | 60 |
| L10-6022 | L10 - Fire Alarm / Elec Specialties RI | 8 | 8 | 17-Mar-14 | 26-Mar-14 | 75 |
| L10-6024 | L10 - Inspections | 2 | 2 | 31-Mar-14 | 01-Apr-14 | 48 |
| **Level 11 - (Guest Rooms)** | | | | | | |
| L11-6000 | L11 - Grind & Patch Lid (Above) | 4 | 4 | 03-Mar-14 | 06-Mar-14 | 48 |
| L11-6002 | L11 - Layout | 1 | 1 | 07-Mar-14 | 07-Mar-14 | 48 |
| L11-6004 | L11 - CMU Walls | 5 | 5 | 10-Mar-14 | 14-Mar-14 | 48 |
| L11-6008 | L11 - Int Wall Framing | 5 | 5 | 17-Mar-14 | 21-Mar-14 | 48 |
| L11-6010 | L11 - CMU Seismic Clips | 1 | 1 | 17-Mar-14 | 17-Mar-14 | 62 |
| L11-6012 | L11 - Fire Sprinkler RI | 10 | 10 | 24-Mar-14 | 04-Apr-14 | 48 |
| L11-6014 | L11 - Plumbing RI | 10 | 10 | 24-Mar-14 | 04-Apr-14 | 48 |
| L11-6016 | L11 - Electrical RI | 10 | 10 | 24-Mar-14 | 04-Apr-14 | 48 |
| L11-6018 | L11 - HVAC RI | 10 | 10 | 24-Mar-14 | 04-Apr-14 | 48 |
| L11-6020 | L11 - H Mtl Frames | 3 | 3 | 24-Mar-14 | 26-Mar-14 | 60 |
| L11-6022 | L11 - Fire Alarm / Elec Specialties RI | 8 | 8 | 24-Mar-14 | 02-Apr-14 | 75 |
| L11-6024 | L11 - Inspections | 2 | 2 | 07-Apr-14 | 08-Apr-14 | 48 |
| **Level 12 - (Guest Rooms)** | | | | | | |

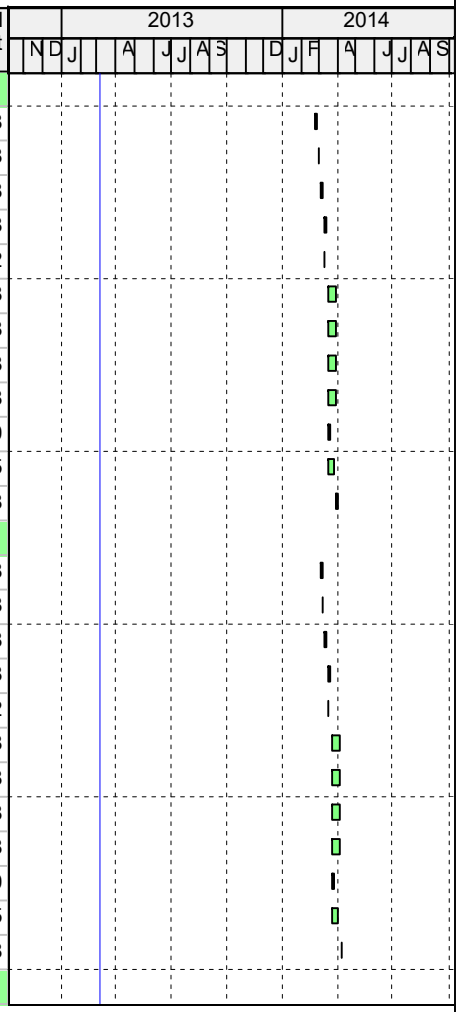



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-6000 | L12 - Grind & Patch Lid (Above) | 4 | 4 | 10-Mar-14 | 13-Mar-14 | 48 |
| L12-6002 | L12 - Layout | 1 | 1 | 14-Mar-14 | 14-Mar-14 | 48 |
| L12-6004 | L12 - CMU Walls | 5 | 5 | 17-Mar-14 | 21-Mar-14 | 48 |
| L12-6008 | L12 - Int Wall Framing | 5 | 5 | 24-Mar-14 | 28-Mar-14 | 48 |
| L12-6010 | L12 - CMU Seismic Clips | 1 | 1 | 24-Mar-14 | 24-Mar-14 | 62 |
| L12-6012 | L12 - Fire Sprinkler RI | 10 | 10 | 31-Mar-14 | 11-Apr-14 | 48 |
| L12-6014 | L12 - Plumbing RI | 10 | 10 | 31-Mar-14 | 11-Apr-14 | 48 |
| L12-6016 | L12 - Electrical RI | 10 | 10 | 31-Mar-14 | 11-Apr-14 | 48 |
| L12-6018 | L12 - HVAC RI | 10 | 10 | 31-Mar-14 | 11-Apr-14 | 48 |
| L12-6020 | L12 - H Mtl Frames | 3 | 3 | 31-Mar-14 | 02-Apr-14 | 60 |
| L12-6022 | L12 - Fire Alarm / Elec Specialties RI | 8 | 8 | 31-Mar-14 | 09-Apr-14 | 75 |
| L12-6024 | L12 - Inspections | 2 | 2 | 14-Apr-14 | 15-Apr-14 | 48 |
| **Level 14 - (Guest Rooms)** | | | | | | |
| L14-6000 | L14 - Grind & Patch Lid (Above) | 4 | 4 | 17-Mar-14 | 20-Mar-14 | 48 |
| L14-6002 | L14 - Layout | 1 | 1 | 21-Mar-14 | 21-Mar-14 | 48 |
| L14-6004 | L14 - CMU Walls | 5 | 5 | 24-Mar-14 | 28-Mar-14 | 48 |
| L14-6008 | L14 - Int Wall Framing | 5 | 5 | 31-Mar-14 | 04-Apr-14 | 48 |
| L14-6010 | L14 - CMU Seismic Clips | 1 | 1 | 31-Mar-14 | 31-Mar-14 | 62 |
| L14-6012 | L14 - Fire Sprinkler RI | 10 | 10 | 07-Apr-14 | 18-Apr-14 | 48 |
| L14-6014 | L14 - Plumbing RI | 10 | 10 | 07-Apr-14 | 18-Apr-14 | 48 |
| L14-6016 | L14 - Electrical RI | 10 | 10 | 07-Apr-14 | 18-Apr-14 | 48 |
| L14-6018 | L14 - HVAC RI | 10 | 10 | 07-Apr-14 | 18-Apr-14 | 48 |
| L14-6020 | L14 - H Mtl Frames | 3 | 3 | 07-Apr-14 | 09-Apr-14 | 60 |
| L14-6022 | L14 - Fire Alarm / Elec Specialties RI | 8 | 8 | 07-Apr-14 | 16-Apr-14 | 75 |
| L14-6024 | L14 - Inspections | 2 | 2 | 21-Apr-14 | 22-Apr-14 | 48 |
| **Level 15 - (Guest Rooms)** | | | | | | |
| L15-6000 | L15 - Grind & Patch Lid (Above) | 4 | 4 | 24-Mar-14 | 27-Mar-14 | 48 |

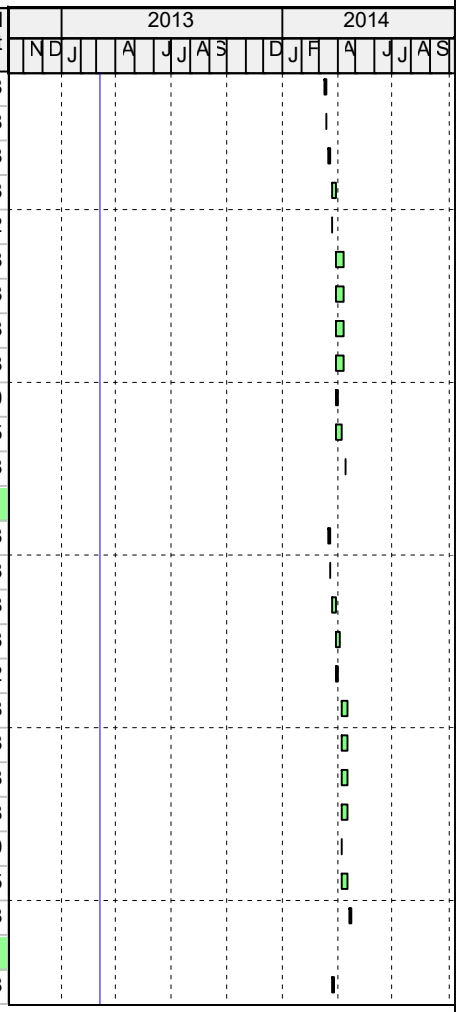



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6002 | L15 - Layout | 1 | 1 | 28-Mar-14 | 28-Mar-14 | 48 |
| L15-6004 | L15 - CMU Walls | 5 | 5 | 31-Mar-14 | 04-Apr-14 | 48 |
| L15-6008 | L15 - Int Wall Framing | 5 | 5 | 07-Apr-14 | 11-Apr-14 | 48 |
| L15-6010 | L15 - CMU Seismic Clips | 1 | 1 | 07-Apr-14 | 07-Apr-14 | 62 |
| L15-6012 | L15 - Fire Sprinkler RI | 10 | 10 | 14-Apr-14 | 25-Apr-14 | 48 |
| L15-6014 | L15 - Plumbing RI | 10 | 10 | 14-Apr-14 | 25-Apr-14 | 48 |
| L15-6016 | L15 - Electrical RI | 10 | 10 | 14-Apr-14 | 25-Apr-14 | 48 |
| L15-6018 | L15 - HVAC RI | 10 | 10 | 14-Apr-14 | 25-Apr-14 | 48 |
| L15-6020 | L15 - H Mtl Frames | 3 | 3 | 14-Apr-14 | 16-Apr-14 | 60 |
| L15-6022 | L15 - Fire Alarm / Elec Specialties RI | 8 | 8 | 14-Apr-14 | 23-Apr-14 | 75 |
| L15-6024 | L15 - Inspections | 2 | 2 | 28-Apr-14 | 29-Apr-14 | 48 |
| **Level 16 - (Guest Rooms)** | | | | | | |
| L16-6000 | L16 - Grind & Patch Lid (Above) | 4 | 4 | 31-Mar-14 | 03-Apr-14 | 48 |
| L16-6002 | L16 - Layout | 1 | 1 | 04-Apr-14 | 04-Apr-14 | 48 |
| L16-6004 | L16 - CMU Walls | 5 | 5 | 07-Apr-14 | 11-Apr-14 | 48 |
| L16-6008 | L16 - Int Wall Framing | 5 | 5 | 14-Apr-14 | 18-Apr-14 | 48 |
| L16-6010 | L16 - CMU Seismic Clips | 1 | 1 | 14-Apr-14 | 14-Apr-14 | 62 |
| L16-6012 | L16 - Fire Sprinkler RI | 10 | 10 | 21-Apr-14 | 02-May-14 | 48 |
| L16-6014 | L16 - Plumbing RI | 10 | 10 | 21-Apr-14 | 02-May-14 | 48 |
| L16-6016 | L16 - Electrical RI | 10 | 10 | 21-Apr-14 | 02-May-14 | 48 |
| L16-6018 | L16 - HVAC RI | 10 | 10 | 21-Apr-14 | 02-May-14 | 48 |
| L16-6020 | L16 - H Mtl Frames | 3 | 3 | 21-Apr-14 | 23-Apr-14 | 60 |
| L16-6022 | L16 - Fire Alarm / Elec Specialties RI | 8 | 8 | 21-Apr-14 | 30-Apr-14 | 75 |
| L16-6024 | L16 - Inspections | 2 | 2 | 05-May-14 | 06-May-14 | 48 |
| **Level 17 - (Guest Rooms)** | | | | | | |
| L17-6000 | L17 - Grind & Patch Lid (Above) | 4 | 4 | 07-Apr-14 | 10-Apr-14 | 48 |
| L17-6002 | L17 - Layout | 1 | 1 | 11-Apr-14 | 11-Apr-14 | 48 |

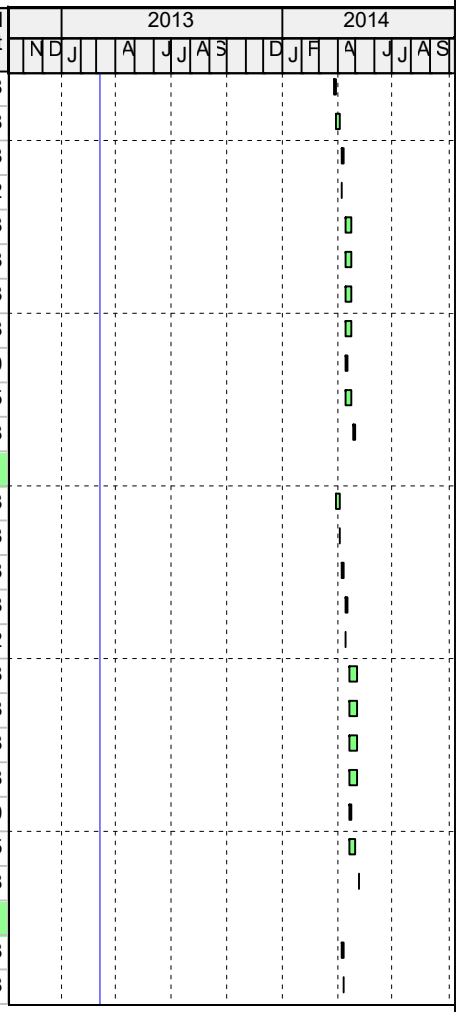



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6004 | L17 - CMU Walls | 5 | 5 | 14-Apr-14 | 18-Apr-14 | 48 |
| L17-6008 | L17 - Int Wall Framing | 5 | 5 | 21-Apr-14 | 25-Apr-14 | 48 |
| L17-6010 | L17 - CMU Seismic Clips | 1 | 1 | 21-Apr-14 | 21-Apr-14 | 62 |
| L17-6012 | L17 - Fire Sprinkler RI | 10 | 10 | 28-Apr-14 | 09-May-14 | 48 |
| L17-6014 | L17 - Plumbing RI | 10 | 10 | 28-Apr-14 | 09-May-14 | 48 |
| L17-6016 | L17 - Electrical RI | 10 | 10 | 28-Apr-14 | 09-May-14 | 48 |
| L17-6018 | L17 - HVAC RI | 10 | 10 | 28-Apr-14 | 09-May-14 | 48 |
| L17-6020 | L17 - H Mtl Frames | 3 | 3 | 28-Apr-14 | 30-Apr-14 | 60 |
| L17-6022 | L17 - Fire Alarm / Elec Specialties RI | 8 | 8 | 28-Apr-14 | 07-May-14 | 75 |
| L17-6024 | L17 - Inspections | 2 | 2 | 12-May-14 | 13-May-14 | 48 |
| **Mechanical Penthouse** | | | | | | |
| PH-6002 | PH - Layout | 1 | 1 | 14-Apr-14 | 14-Apr-14 | 49 |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 5 | 15-Apr-14 | 21-Apr-14 | 60 |
| PH-6006 | PH - Ext Wall Framing - (Incldg Roof Parapet) | 10 | 10 | 15-Apr-14 | 28-Apr-14 | 49 |
| PH-6008 | PH - Int Wall Framing | 3 | 3 | 29-Apr-14 | 01-May-14 | 49 |
| PH-6012 | PH - Fire Sprinkler RI | 8 | 8 | 02-May-14 | 13-May-14 | 56 |
| PH-6014 | PH - Plumbing RI | 12 | 12 | 02-May-14 | 19-May-14 | 52 |
| PH-6016 | PH - Electrical RI | 12 | 12 | 02-May-14 | 19-May-14 | 52 |
| PH-6018 | PH - HVAC RI | 15 | 15 | 02-May-14 | 22-May-14 | 49 |
| PH-6020 | PH - H Mtl Frames | 2 | 2 | 02-May-14 | 05-May-14 | 67 |
| PH-6022 | PH - Fire Alarm / Elec Specialties RI | 5 | 5 | 02-May-14 | 08-May-14 | 80 |
| PH-6024 | PH - Inspections | 2 | 2 | 23-May-14 | 27-May-14 | 49 |
| **Finishes** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL4-8100 | LL4 - Insulation | 1 | 1 | 10-Mar-14 | 10-Mar-14 | 0 |

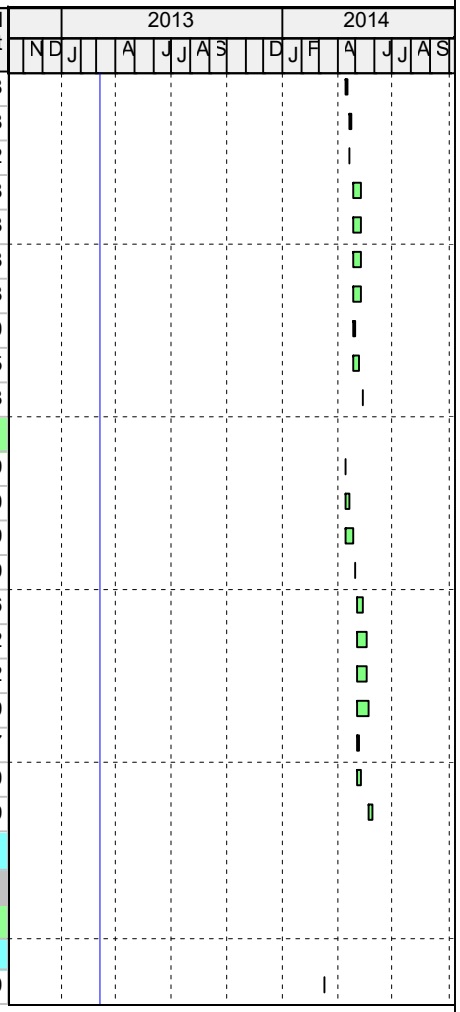



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8102 | LL4 - GWB Hang / Tape / Finish - (Including Commor | 5 | 5 | 11-Mar-14 | 17-Mar-14 | 0 |
| LL4-6026 | LL4 - Pull Wire | 6 | 6 | 11-Mar-14 | 18-Mar-14 | 73 |
| LL4-8104 | LL4 - Int Painting | 3 | 3 | 13-Mar-14 | 17-Mar-14 | 67 |
| LL4-8108 | LL4 - Elec Trim / Finish | 6 | 6 | 18-Mar-14 | 25-Mar-14 | 68 |
| LL4-8110 | LL4 - HVAC Trim / Finish | 6 | 6 | 18-Mar-14 | 25-Mar-14 | 68 |
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 5 | 5 | 18-Mar-14 | 24-Mar-14 | 69 |
| LL4-8114 | LL4 - Striping / Signage | 3 | 3 | 18-Mar-14 | 20-Mar-14 | 80 |
| LL4-8118 | LL4 - Elec Specialties Trim / Finish | 4 | 4 | 18-Mar-14 | 21-Mar-14 | 70 |
| LL4-8122 | LL4 - Plumbing Trim / Finish | 5 | 5 | 26-Mar-14 | 01-Apr-14 | 67 |
| LL4-8124 | LL4 - Flooring | 3 | 3 | 26-Mar-14 | 28-Mar-14 | 68 |
| LL4-8126 | LL4 - Doors & Hardware | 3 | 3 | 27-Mar-14 | 31-Mar-14 | 68 |
| LL4-8130 | LL4 - Substantially Complete | 0 | 0 | | 01-Apr-14 | 67 |
| LL4-8132 | LL4 - Contractor Pre-Punchlist | 5 | 5 | 02-Apr-14 | 08-Apr-14 | 70 |
| LL4-8134 | LL4 - Pre-Clean | 5 | 5 | 02-Apr-14 | 08-Apr-14 | 67 |
| LL4-8208 | LL4 - Final Clean | 3 | 3 | 09-Apr-14 | 11-Apr-14 | 67 |
| LL4-8210 | LL4 - Owner Walk / Create Punchlist | 1 | 1 | 14-Apr-14 | 14-Apr-14 | 67 |
| LL4-8212 | LL4 - Final Punchlist | 5 | 5 | 15-Apr-14 | 21-Apr-14 | 67 |
| LL4-8214 | LL4 - Floor Complete | 0 | 0 | | 21-Apr-14 | 67 |
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL3-8100 | LL3 - Insulation | 1 | 1 | 11-Mar-14 | 11-Mar-14 | 0 |
| LL3-6026 | LL3 - Pull Wire | 6 | 6 | 12-Mar-14 | 19-Mar-14 | 77 |
| LL3-8102 | LL3 - GWB Hang / Tape / Finish - (Including Commor | 5 | 5 | 14-Mar-14 | 20-Mar-14 | 0 |
| LL3-8104 | LL3 - Int Painting | 3 | 3 | 18-Mar-14 | 20-Mar-14 | 69 |
| LL3-8108 | LL3 - Elec Trim / Finish | 6 | 6 | 21-Mar-14 | 28-Mar-14 | 70 |
| LL3-8110 | LL3 - HVAC Trim / Finish | 6 | 6 | 21-Mar-14 | 28-Mar-14 | 70 |
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 5 | 5 | 21-Mar-14 | 27-Mar-14 | 71 |

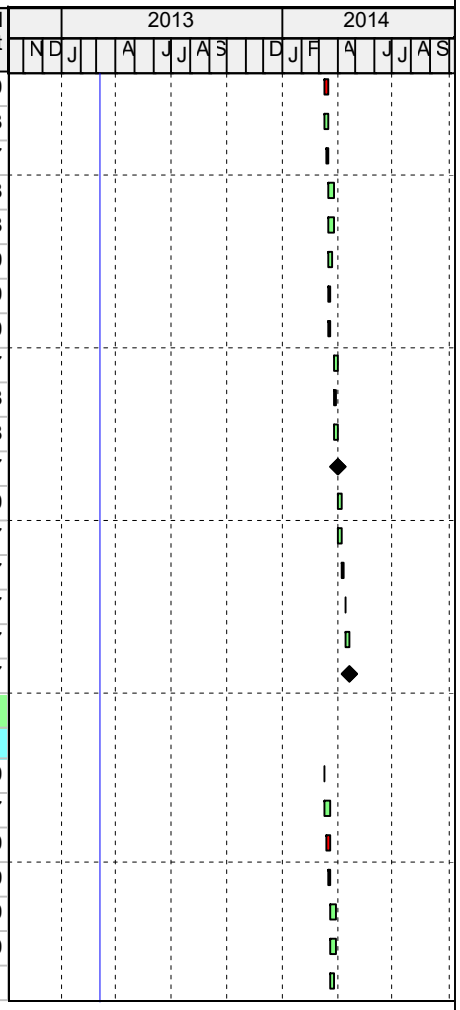



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-8114 | LL3 - Striping / Signage | 3 | 3 | 21-Mar-14 | 25-Mar-14 | 82 |
| LL3-8118 | LL3 - Elec Specialties Trim / Finish | 4 | 4 | 21-Mar-14 | 26-Mar-14 | 72 |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 5 | 5 | 31-Mar-14 | 04-Apr-14 | 69 |
| LL3-8124 | LL3 - Flooring | 3 | 3 | 31-Mar-14 | 02-Apr-14 | 70 |
| LL3-8126 | LL3 - Doors & Hardware | 3 | 3 | 01-Apr-14 | 03-Apr-14 | 70 |
| LL3-8130 | LL3 - Substantially Complete | 0 | 0 | | 04-Apr-14 | 69 |
| LL3-8132 | LL3 - Contractor Pre-Punchlist | 5 | 5 | 07-Apr-14 | 11-Apr-14 | 72 |
| LL3-8134 | LL3 - Pre-Clean | 5 | 5 | 07-Apr-14 | 11-Apr-14 | 69 |
| LL3-8208 | LL3 - Final Clean | 3 | 3 | 14-Apr-14 | 16-Apr-14 | 69 |
| LL3-8210 | LL3 - Owner Walk / Create Punchlist | 1 | 1 | 17-Apr-14 | 17-Apr-14 | 69 |
| LL3-8212 | LL3 - Final Punchlist | 5 | 5 | 22-Apr-14 | 28-Apr-14 | 67 |
| LL3-8214 | LL3 - Floor Complete | 0 | 0 | | 28-Apr-14 | 67 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL2-8100 | LL2 - Insulation | 5 | 5 | 12-Mar-14 | 18-Mar-14 | 0 |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish - (Including Commor | 15 | 15 | 19-Mar-14 | 08-Apr-14 | 0 |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 10 | 10 | 19-Mar-14 | 01-Apr-14 | 72 |
| LL2-6026 | LL2 - Pull Wire | 15 | 15 | 19-Mar-14 | 08-Apr-14 | 66 |
| LL2-8128 | LL2 - Entry Gates | 3 | 3 | 02-Apr-14 | 04-Apr-14 | 72 |
| LL2-8104 | LL2 - Int Painting | 5 | 5 | 04-Apr-14 | 10-Apr-14 | 44 |
| LL2-8136 | LL2 - Chainlink Fencing / Gate @ Recycling | 2 | 2 | 07-Apr-14 | 08-Apr-14 | 72 |
| LL2-8120 | LL2 - Steel Pipe Guardrails | 6 | 6 | 09-Apr-14 | 16-Apr-14 | 66 |
| LL2-8108 | LL2 - Elec Trim / Finish | 20 | 20 | 11-Apr-14 | 08-May-14 | 44 |
| LL2-8110 | LL2 - HVAC Trim / Finish | 12 | 12 | 11-Apr-14 | 28-Apr-14 | 52 |
| LL2-8112 | LL2 - Fire Sprinkler Trim / Finish | 8 | 8 | 11-Apr-14 | 22-Apr-14 | 56 |
| LL2-8114 | LL2 - Striping / Signage | 3 | 3 | 11-Apr-14 | 15-Apr-14 | 72 |
| LL2-8116 | LL2 - Finish Carpentry / Millwork | 2 | 2 | 11-Apr-14 | 14-Apr-14 | 61 |

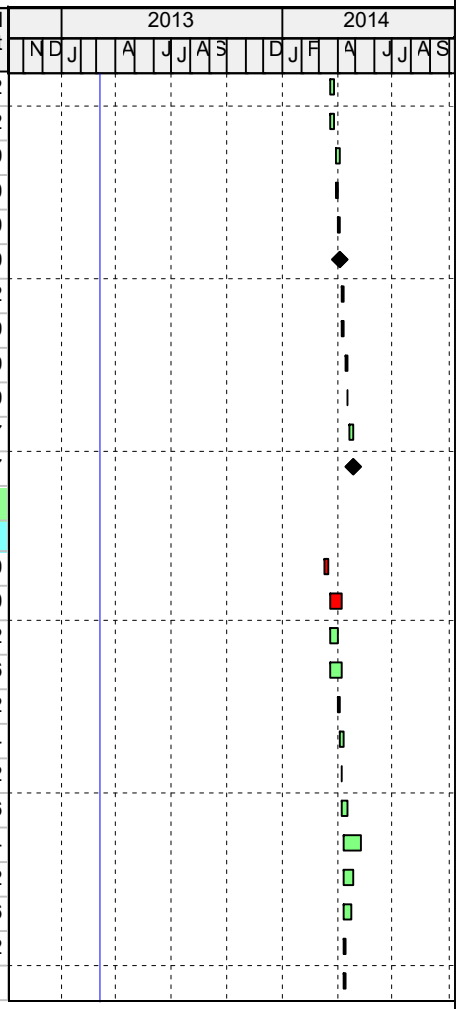



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-8118 | LL2 - Elec Specialties Trim / Finish | 4 | 4 | 11-Apr-14 | 16-Apr-14 | 60 |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 9 | 9 | 11-Apr-14 | 23-Apr-14 | 61 |
| LL2-8122 | LL2 - Plumbing Trim / Finish | 5 | 5 | 17-Apr-14 | 23-Apr-14 | 61 |
| LL2-8126 | LL2 - Doors & Hardware | 7 | 7 | 08-May-14 | 16-May-14 | 44 |
| LL2-8124 | LL2 - Flooring | 5 | 5 | 09-May-14 | 15-May-14 | 44 |
| LL2-8130 | LL2 - Substantially Complete | 0 | 0 | | 16-May-14 | 44 |
| LL2-8132 | LL2 - Contractor Pre-Punchlist | 5 | 5 | 19-May-14 | 23-May-14 | 47 |
| LL2-8134 | LL2 - Pre-Clean | 5 | 5 | 19-May-14 | 23-May-14 | 44 |
| LL2-8208 | LL2 - Final Clean | 3 | 3 | 27-May-14 | 29-May-14 | 44 |
| LL2-8210 | LL2 - Owner Walk / Create Punchlist | 1 | 1 | 30-May-14 | 30-May-14 | 44 |
| LL2-8212 | LL2 - Final Punchlist | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 44 |
| LL2-8214 | LL2 - Floor Complete | 0 | 0 | | 06-Jun-14 | 44 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1-8100 | LL1 - Insulation | 5 | 5 | 19-Mar-14 | 25-Mar-14 | 1 |
| LL1-6026 | LL1 - Pull Wire | 10 | 10 | 26-Mar-14 | 08-Apr-14 | 38 |
| LL1-8102 | LL1 - GWB Hang / Tape / Finish - (Including Commor | 20 | 20 | 27-Mar-14 | 23-Apr-14 | 0 |
| LL1-8104 | LL1 - Int Painting | 10 | 10 | 21-Apr-14 | 02-May-14 | 0 |
| LL1-8106 | LL1 - Wallcoverings | 6 | 6 | 23-Apr-14 | 30-Apr-14 | 22 |
| LL1-8116 | LL1 - Finish Carpentry / Millwork | 10 | 10 | 28-Apr-14 | 09-May-14 | 11 |
| LL1-8120 | LL1 - Ceramic Tile / Counter Tops | 12 | 12 | 30-Apr-14 | 15-May-14 | 11 |
| LL1-8122 | LL1 - Plumbing Trim / Finish | 10 | 10 | 02-May-14 | 15-May-14 | 17 |
| LL1-8112 | LL1 - Fire Sprinkler Trim / Finish | 8 | 8 | 05-May-14 | 14-May-14 | 12 |
| LL1-8118 | LL1 - Elec Specialties Trim / Finish | 6 | 6 | 05-May-14 | 12-May-14 | 14 |
| LL1-8114 | LL1 - T-Bar Grid Ceiling | 8 | 8 | 05-May-14 | 14-May-14 | 0 |
| LL1-8138 | LL1 - Epoxy Flooring @ Food Prep | 7 | 7 | 12-May-14 | 20-May-14 | 17 |
| LL1-8142 | LL1 - Folding Partitions @ Meeting Rooms | 8 | 8 | 12-May-14 | 21-May-14 | 16 |

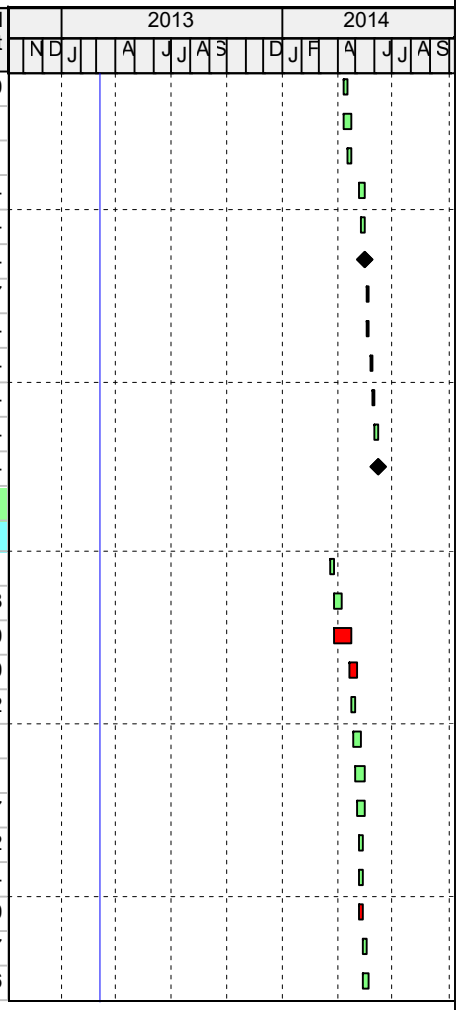



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-8108 | LL1 - Elec Trim / Finish | 12 | 12 | 15-May-14 | 02-Jun-14 | 0 |
| LL1-8110 | LL1 - HVAC Trim / Finish | 10 | 10 | 15-May-14 | 29-May-14 | 2 |
| LL1-8128 | LL1 - Bath Specialties | 3 | 3 | 16-May-14 | 20-May-14 | 17 |
| LL1-8136 | LL1 - Toilet Partitions | 3 | 3 | 16-May-14 | 20-May-14 | 17 |
| LL1-8124 | LL1 - Flooring @ Meeting Rooms | 8 | 8 | 03-Jun-14 | 12-Jun-14 | 0 |
| LL1-8140 | LL1 - Acoustical Ceiling Tile | 5 | 5 | 03-Jun-14 | 09-Jun-14 | 4 |
| LL1-8126 | LL1 - Doors & Hardware | 8 | 8 | 04-Jun-14 | 13-Jun-14 | 0 |
| LL1-8130 | LL1 - Meeting Rooms / Food Prep Substantially Com | 0 | 0 | | 13-Jun-14 | 0 |
| LL1-8132 | LL1 - Contractor Pre-Punchlist | 10 | 10 | 16-Jun-14 | 27-Jun-14 | 28 |
| LL1-8134 | LL1 - Pre-Clean | 8 | 8 | 16-Jun-14 | 25-Jun-14 | 25 |
| **Corridors / Common / Public Areas** | | | | | | |
| LL1-8200 | LL1 - Final Paint @ Common / Public Areas | 6 | 6 | 16-Jun-14 | 23-Jun-14 | 0 |
| LL1-8202 | LL1 - Elec Trim / Finish @ Common / Public Areas | 10 | 10 | 24-Jun-14 | 08-Jul-14 | 0 |
| LL1-8204 | LL1 - Mech Trim / Finish @ Common / Public Areas | 8 | 8 | 24-Jun-14 | 03-Jul-14 | 2 |
| LL1-8206 | LL1 - Flooring @ Common / Public Areas | 6 | 6 | 08-Jul-14 | 15-Jul-14 | 12 |
| LL1-8208 | LL1 - Final Clean | 5 | 5 | 16-Jul-14 | 22-Jul-14 | 12 |
| LL1-8210 | LL1 - Owner Walk / Create Punchlist | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 12 |
| LL1-8212 | LL1 - Final Punchlist | 10 | 10 | 24-Jul-14 | 06-Aug-14 | 12 |
| LL1-8214 | LL1 - Floor Complete | 0 | 0 | | 06-Aug-14 | 12 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| **Main Ballrooms / Meeting Rooms / Kitchen / Lobby / Dining** | | | | | | |
| L01-8100 | L1 - Insulation | 5 | 5 | 20-Mar-14 | 26-Mar-14 | 10 |
| L01-6026 | L1 - Pull Wire | 10 | 10 | 20-Mar-14 | 02-Apr-14 | 44 |
| L01-8102 | L1 - GWB Hang / Tape / Finish - (Including Common / | 20 | 20 | 03-Apr-14 | 30-Apr-14 | 5 |
| L01-8104 | L1 - Int Painting | 10 | 10 | 28-Apr-14 | 09-May-14 | 5 |
| L01-8106 | L1 - Wallcoverings | 6 | 6 | 30-Apr-14 | 07-May-14 | 19 |
| L01-8116 | L1 - Finish Carpentry / Millwork | 14 | 14 | 05-May-14 | 22-May-14 | 8 |

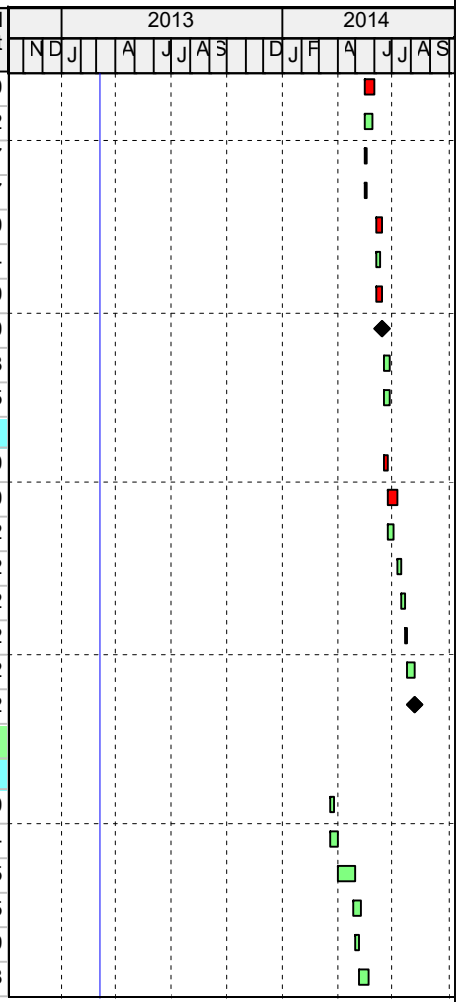



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L01-8120 | L1 - Ceramic Tile / Counter Tops @ Restrooms | 12 | 12 | 07-May-14 | 22-May-14 | 8 |
| L01-8122 | L1 - Plumbing Trim / Finish | 10 | 10 | 09-May-14 | 22-May-14 | 14 |
| L01-8108 | L1 - Elec Trim / Finish | 12 | 12 | 12-May-14 | 28-May-14 | 5 |
| L01-8110 | L1 - HVAC Trim / Finish | 10 | 10 | 12-May-14 | 23-May-14 | 7 |
| L01-8112 | L1 - Fire Sprinkler Trim / Finish | 8 | 8 | 12-May-14 | 21-May-14 | 9 |
| L01-8118 | L1 - Elec Specialties Trim / Finish | 6 | 6 | 12-May-14 | 19-May-14 | 11 |
| L01-8136 | L1 - Casework / Front Desk | 10 | 10 | 12-May-14 | 23-May-14 | 16 |
| L01-8140 | L1 - Tile Flooring @ Kitchen | 12 | 12 | 12-May-14 | 28-May-14 | 14 |
| L01-8142 | L1 - Folding Partitions @ Ballrooms | 10 | 10 | 12-May-14 | 23-May-14 | 16 |
| L01-8128 | L1 - Bath Specialties | 3 | 3 | 23-May-14 | 28-May-14 | 14 |
| L01-8138 | L1 - Toilet Partitions | 3 | 3 | 23-May-14 | 28-May-14 | 14 |
| L01-8124 | L1 - Flooring @ Ballrooms | 8 | 8 | 29-May-14 | 09-Jun-14 | 5 |
| L01-8126 | L1 - Doors & Hardware | 8 | 8 | 30-May-14 | 10-Jun-14 | 5 |
| L01-8130 | L1 - Ballrooms / Kitchen / Restrooms Substantially Cc | 0 | 0 | | 10-Jun-14 | 5 |
| L01-8132 | L1 - Contractor Pre-Punchlist | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 36 |
| L01-8134 | L1 - Pre-Clean | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 31 |
| L01-8114 | L1 - Signage | 3 | 3 | 19-Jun-14 | 23-Jun-14 | 27 |
| **Corridors / Common / Public Areas** | | | | | | |
| L01-8200 | L1 - Final Paint @ Common / Public Areas | 6 | 6 | 11-Jun-14 | 18-Jun-14 | 5 |
| L01-8202 | L1 - Elec Trim / Finish @ Common / Public Areas | 8 | 8 | 19-Jun-14 | 30-Jun-14 | 5 |
| L01-8204 | L1 - Mech Trim / Finish @ Common / Public Areas | 8 | 8 | 19-Jun-14 | 30-Jun-14 | 5 |
| L01-8206 | L1 - Flooring @ Common / Public Areas | 10 | 10 | 30-Jun-14 | 14-Jul-14 | 13 |
| L01-8208 | L1 - Final Clean | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 13 |
| L01-8216 | L1 - Entry Mats | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 16 |
| L01-8210 | L1 - Owner Walk / Create Punchlist | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 13 |
| L01-8212 | L1 - Final Punchlist | 10 | 10 | 23-Jul-14 | 05-Aug-14 | 13 |
| L01-8214 | L1 - Floor Complete | 0 | 0 | | 05-Aug-14 | 13 |

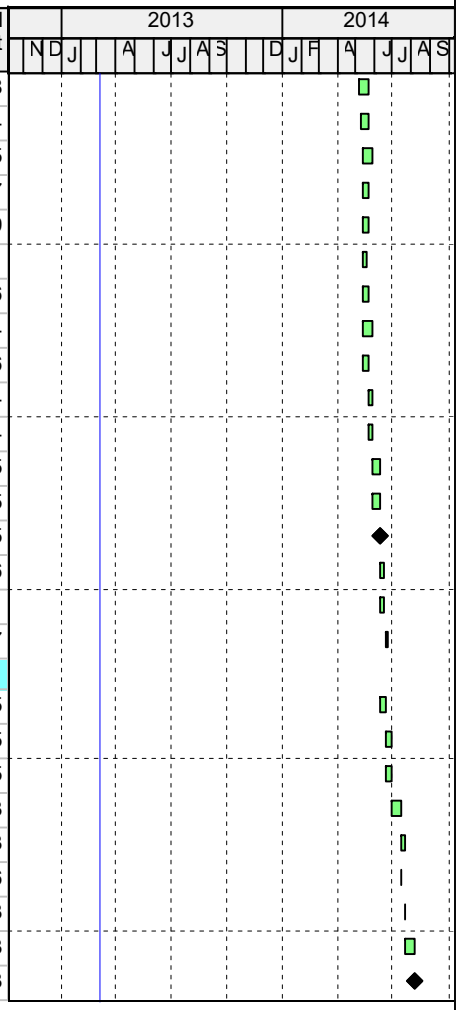



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8100 | L2 - Insulation | 5 | 5 | 24-Mar-14 | 28-Mar-14 | 23 |
| L02-6026 | L2 - Pull Wire | 6 | 6 | 24-Mar-14 | 31-Mar-14 | 46 |
| L02-8102 | L2 - GWB Hang / Tape / Finish - (Including Common / | 16 | 16 | 17-Apr-14 | 08-May-14 | 10 |
| L02-8104 | L2 - Int Painting | 8 | 8 | 06-May-14 | 15-May-14 | 10 |
| L02-8106 | L2 - Wallcoverings | 6 | 6 | 08-May-14 | 15-May-14 | 20 |
| L02-8116 | L2 - Finish Carpentry / Millwork | 5 | 5 | 13-May-14 | 19-May-14 | 13 |
| L02-8120 | L2 - Ceramic Tile / Counter Tops | 8 | 8 | 15-May-14 | 27-May-14 | 13 |
| L02-8108 | L2 - Elec Trim / Finish | 10 | 10 | 16-May-14 | 30-May-14 | 10 |
| L02-8110 | L2 - HVAC Trim / Finish | 10 | 10 | 16-May-14 | 30-May-14 | 10 |
| L02-8112 | L2 - Fire Sprinkler Trim / Finish | 8 | 8 | 16-May-14 | 28-May-14 | 12 |
| L02-8118 | L2 - Elec Specialties Trim / Finish | 6 | 6 | 16-May-14 | 23-May-14 | 14 |
| L02-8136 | L2 - Lockers / Benches @ Locker Rooms | 5 | 5 | 16-May-14 | 22-May-14 | 21 |
| L02-8122 | L2 - Plumbing Trim / Finish | 8 | 8 | 19-May-14 | 29-May-14 | 15 |
| L02-8128 | L2 - Bath Specialties | 2 | 2 | 30-May-14 | 02-Jun-14 | 15 |
| L02-8124 | L2 - Flooring | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 10 |
| L02-8126 | L2 - Doors & Hardware | 5 | 5 | 03-Jun-14 | 09-Jun-14 | 10 |
| L02-8130 | L2 - Admin / Employee Rooms Substantially Complet | 0 | 0 | | 09-Jun-14 | 10 |
| L02-8132 | L2 - Contractor Pre-Punchlist | 5 | 5 | 10-Jun-14 | 16-Jun-14 | 42 |
| L02-8134 | L2 - Pre-Clean | 5 | 5 | 10-Jun-14 | 16-Jun-14 | 39 |
| **Corridors** | | | | | | |
| L02-8200 | L2 - Final Paint @ Common / Public Areas | 5 | 5 | 10-Jun-14 | 16-Jun-14 | 10 |
| L02-8114 | L2 - Signage | 3 | 3 | 17-Jun-14 | 19-Jun-14 | 36 |
| L02-8202 | L2 - Elec Trim / Finish @ Common / Public Areas | 5 | 5 | 17-Jun-14 | 23-Jun-14 | 10 |
| L02-8204 | L2 - Mech Trim / Finish @ Common / Public Areas | 5 | 5 | 17-Jun-14 | 23-Jun-14 | 10 |
| L02-8206 | L2 - Flooring @ Corridors | 3 | 3 | 24-Jun-14 | 26-Jun-14 | 31 |

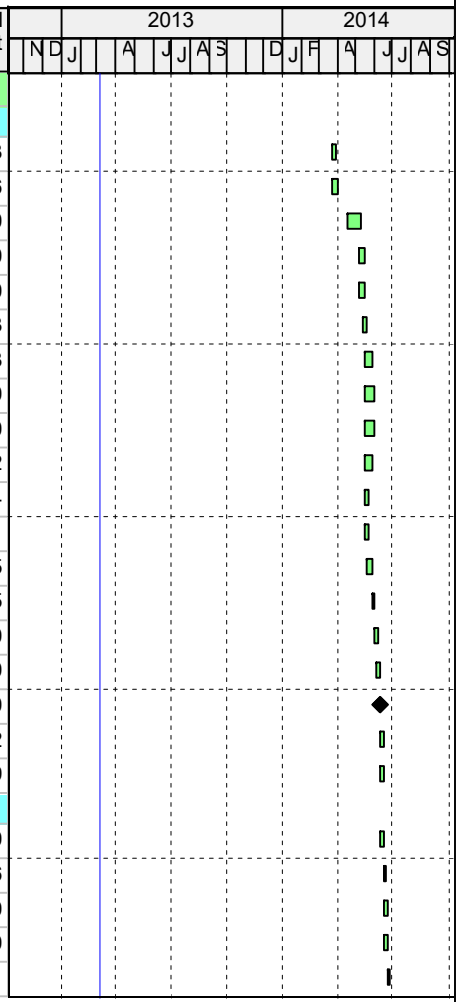


Actual Work | Remaining Work | Critical Remai... | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8208 | L2 - Final Clean | 3 | 3 | 27-Jun-14 | 01-Jul-14 | 31 |
| L02-8210 | L2 - Owner Walk / Create Punchlist | 1 | 1 | 02-Jul-14 | 02-Jul-14 | 31 |
| L02-8212 | L2 - Final Punchlist | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 31 |
| L02-8214 | L2 - Floor Complete | 0 | 0 | | 10-Jul-14 | 31 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L03-6026 | L3 - Pull Wire | 6 | 6 | 17-Mar-14 | 24-Mar-14 | 48 |
| L03-8100 | L3 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 21-Apr-14 | 23-Apr-14 | 0 |
| L03-8102 | L3 - GWB Hang / Tape / Finish - (Including Common / | 14 | 14 | 24-Apr-14 | 13-May-14 | 0 |
| L03-8104 | L3 - Int Painting | 5 | 5 | 09-May-14 | 15-May-14 | 0 |
| L03-8106 | L3 - Wallcoverings | 6 | 6 | 13-May-14 | 20-May-14 | 7 |
| L03-8108 | L3 - Elec Trim / Finish | 8 | 8 | 16-May-14 | 28-May-14 | 2 |
| L03-8110 | L3 - HVAC Trim / Finish | 8 | 8 | 16-May-14 | 28-May-14 | 2 |
| L03-8112 | L3 - Fire Sprinkler Trim / Finish | 8 | 8 | 16-May-14 | 28-May-14 | 2 |
| L03-8116 | L3 - Finish Carpentry / Millwork | 8 | 8 | 16-May-14 | 28-May-14 | 0 |
| L03-8118 | L3 - Elec Specialties Trim / Finish | 4 | 4 | 16-May-14 | 21-May-14 | 6 |
| L03-8120 | L3 - Ceramic Tile / Counter Tops | 8 | 8 | 20-May-14 | 30-May-14 | 0 |
| L03-8122 | L3 - Plumbing Trim / Finish | 8 | 8 | 22-May-14 | 03-Jun-14 | 1 |
| L03-8126 | L3 - Doors & Hardware | 8 | 8 | 29-May-14 | 09-Jun-14 | 0 |
| L03-8124 | L3 - Flooring @ Guest Rooms | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 0 |
| L03-8128 | L3 - Bath Specialties / Tub Glazing | 3 | 3 | 04-Jun-14 | 06-Jun-14 | 1 |
| L03-8130 | L3 - Guest Rooms Substantially Complete | 0 | 0 | | 09-Jun-14 | 0 |
| L03-8114 | L3 - Signage | 3 | 3 | 10-Jun-14 | 12-Jun-14 | 5 |
| L03-8132 | L3 - Contractor Pre-Punchlist | 5 | 5 | 10-Jun-14 | 16-Jun-14 | 6 |
| L03-8134 | L3 - Pre-Clean | 5 | 5 | 10-Jun-14 | 16-Jun-14 | 3 |
| **Pool Area** | | | | | | |

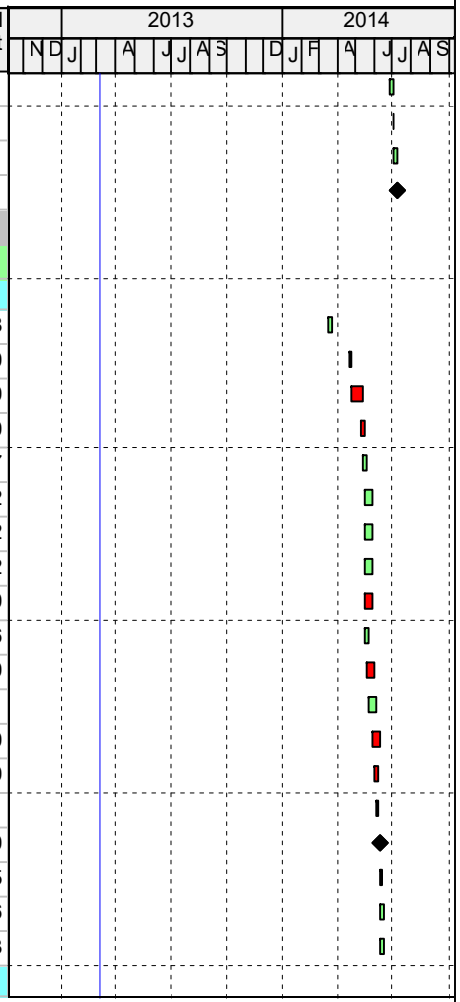



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8216 | L3 - Pool Surfaces / Finishes | 16 | 16 | 16-May-14 | 09-Jun-14 | 12 |
| L03-8218 | L3 - Pool Equipment | 5 | 5 | 10-Jun-14 | 16-Jun-14 | 12 |
| **Corridors / Common / Public Areas** | | | | | | |
| L03-8200 | L3 - Final Paint @ Common / Public Areas | 3 | 3 | 10-Jun-14 | 12-Jun-14 | 0 |
| L03-8202 | L3 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 13-Jun-14 | 17-Jun-14 | 0 |
| L03-8204 | L3 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 13-Jun-14 | 17-Jun-14 | 0 |
| L03-8206 | L3 - Flooring @ Common / Public Areas | 3 | 3 | 17-Jun-14 | 19-Jun-14 | 0 |
| L03-8208 | L3 - Final Clean | 3 | 3 | 20-Jun-14 | 24-Jun-14 | 0 |
| L03-8210 | L3 - Owner Walk / Create Punchlist | 1 | 1 | 25-Jun-14 | 25-Jun-14 | 0 |
| L03-8212 | L3 - Final Punchlist | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 0 |
| L03-8214 | L3 - Floor Complete | 0 | 0 | | 02-Jul-14 | 0 |
| **Level 4 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L04-8100 | L4 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 24-Mar-14 | 26-Mar-14 | 25 |
| L04-6026 | L4 - Pull Wire | 6 | 6 | 24-Mar-14 | 31-Mar-14 | 48 |
| L04-8102 | L4 - GWB Hang / Tape / Finish - (Including Common / | 14 | 14 | 01-May-14 | 20-May-14 | 0 |
| L04-8104 | L4 - Int Painting | 5 | 5 | 16-May-14 | 22-May-14 | 0 |
| L04-8106 | L4 - Wallcoverings | 6 | 6 | 20-May-14 | 28-May-14 | 7 |
| L04-8108 | L4 - Elec Trim / Finish | 8 | 8 | 23-May-14 | 04-Jun-14 | 2 |
| L04-8110 | L4 - HVAC Trim / Finish | 8 | 8 | 23-May-14 | 04-Jun-14 | 2 |
| L04-8112 | L4 - Fire Sprinkler Trim / Finish | 8 | 8 | 23-May-14 | 04-Jun-14 | 2 |
| L04-8116 | L4 - Finish Carpentry / Millwork | 8 | 8 | 23-May-14 | 04-Jun-14 | 0 |
| L04-8118 | L4 - Elec Specialties Trim / Finish | 4 | 4 | 23-May-14 | 29-May-14 | 6 |
| L04-8120 | L4 - Ceramic Tile / Counter Tops | 8 | 8 | 28-May-14 | 06-Jun-14 | 0 |
| L04-8122 | L4 - Plumbing Trim / Finish | 8 | 8 | 30-May-14 | 10-Jun-14 | 1 |
| L04-8124 | L4 - Flooring @ Guest Rooms | 5 | 5 | 09-Jun-14 | 13-Jun-14 | 0 |
| L04-8126 | L4 - Doors & Hardware | 5 | 5 | 10-Jun-14 | 16-Jun-14 | 0 |

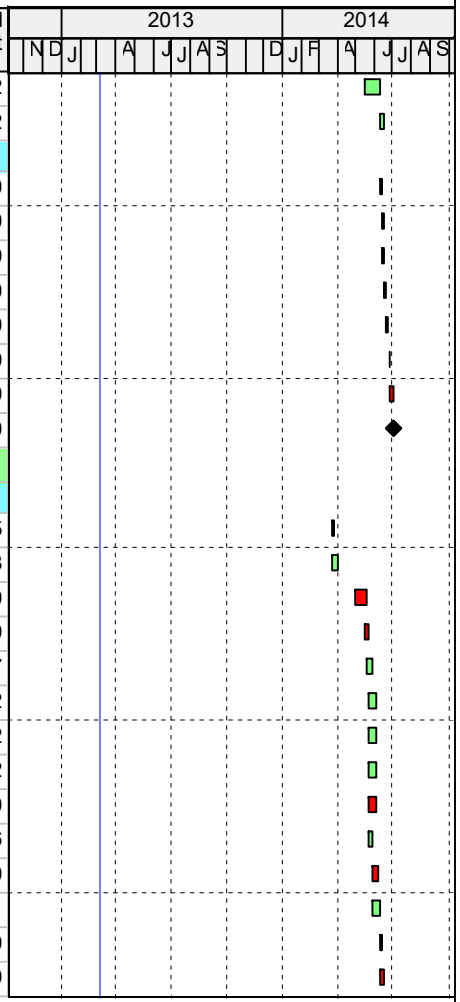



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8128 | L4 - Bath Specialties / Tub Glazing | 3 | 3 | 11-Jun-14 | 13-Jun-14 | 1 |
| L04-8130 | L4 - Guest Rooms Substantially Complete | 0 | 0 | | 16-Jun-14 | 0 |
| L04-8114 | L4 - Signage | 3 | 3 | 17-Jun-14 | 19-Jun-14 | 5 |
| L04-8132 | L4 - Contractor Pre-Punchlist | 5 | 5 | 17-Jun-14 | 23-Jun-14 | 6 |
| L04-8134 | L4 - Pre-Clean | 5 | 5 | 17-Jun-14 | 23-Jun-14 | 3 |
| **Corridors / Common / Public Areas** | | | | | | |
| L04-8200 | L4 - Final Paint @ Common / Public Areas | 3 | 3 | 17-Jun-14 | 19-Jun-14 | 0 |
| L04-8202 | L4 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 20-Jun-14 | 24-Jun-14 | 0 |
| L04-8204 | L4 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 20-Jun-14 | 24-Jun-14 | 0 |
| L04-8206 | L4 - Flooring @ Common / Public Areas | 3 | 3 | 24-Jun-14 | 26-Jun-14 | 0 |
| L04-8208 | L4 - Final Clean | 3 | 3 | 27-Jun-14 | 01-Jul-14 | 0 |
| L04-8210 | L4 - Owner Walk / Create Punchlist | 1 | 1 | 02-Jul-14 | 02-Jul-14 | 0 |
| L04-8212 | L4 - Final Punchlist | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 0 |
| L04-8214 | L4 - Floor Complete | 0 | 0 | | 10-Jul-14 | 0 |
| **Level 5 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L05-8100 | L5 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 31-Mar-14 | 02-Apr-14 | 25 |
| L05-6026 | L5 - Pull Wire | 6 | 6 | 31-Mar-14 | 07-Apr-14 | 48 |
| L05-8102 | L5 - GWB Hang / Tape / Finish - (Including Common / | 14 | 14 | 08-May-14 | 28-May-14 | 0 |
| L05-8104 | L5 - Int Painting | 5 | 5 | 23-May-14 | 30-May-14 | 0 |
| L05-8106 | L5 - Wallcoverings | 6 | 6 | 28-May-14 | 04-Jun-14 | 7 |
| L05-8108 | L5 - Elec Trim / Finish | 8 | 8 | 02-Jun-14 | 11-Jun-14 | 2 |
| L05-8110 | L5 - HVAC Trim / Finish | 8 | 8 | 02-Jun-14 | 11-Jun-14 | 2 |
| L05-8112 | L5 - Fire Sprinkler Trim / Finish | 8 | 8 | 02-Jun-14 | 11-Jun-14 | 2 |
| L05-8116 | L5 - Finish Carpentry / Millwork | 8 | 8 | 02-Jun-14 | 11-Jun-14 | 0 |
| L05-8118 | L5 - Elec Specialties Trim / Finish | 4 | 4 | 02-Jun-14 | 05-Jun-14 | 6 |
| L05-8120 | L5 - Ceramic Tile / Counter Tops | 8 | 8 | 04-Jun-14 | 13-Jun-14 | 0 |

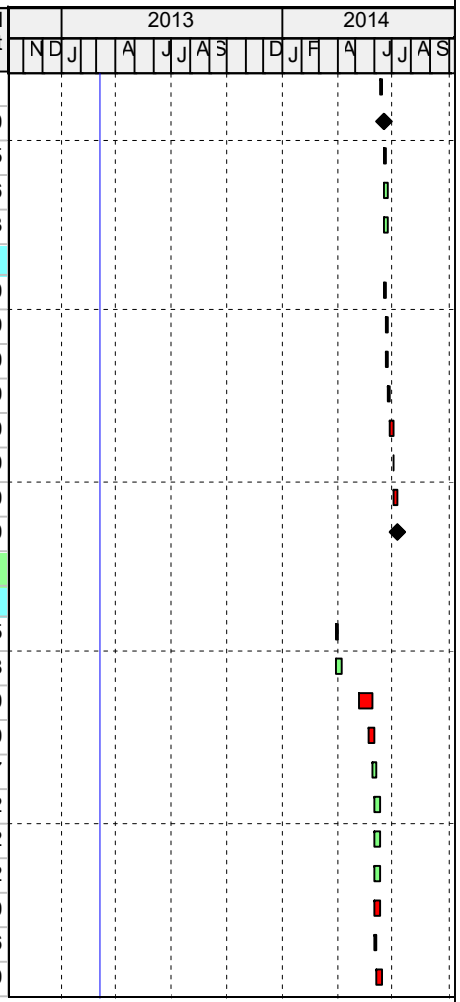



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8122 | L5 - Plumbing Trim / Finish | 8 | 8 | 06-Jun-14 | 17-Jun-14 | 1 |
| L05-8124 | L5 - Flooring @ Guest Rooms | 5 | 5 | 16-Jun-14 | 20-Jun-14 | 0 |
| L05-8126 | L5 - Doors & Hardware | 5 | 5 | 17-Jun-14 | 23-Jun-14 | 0 |
| L05-8128 | L5 - Bath Specialties / Tub Glazing | 3 | 3 | 18-Jun-14 | 20-Jun-14 | 1 |
| L05-8130 | L5 - Guest Rooms Substantially Complete | 0 | 0 | | 23-Jun-14 | 0 |
| L05-8114 | L5 - Signage | 3 | 3 | 24-Jun-14 | 26-Jun-14 | 5 |
| L05-8132 | L5 - Contractor Pre-Punchlist | 5 | 5 | 24-Jun-14 | 30-Jun-14 | 6 |
| L05-8134 | L5 - Pre-Clean | 5 | 5 | 24-Jun-14 | 30-Jun-14 | 3 |
| **Corridors / Common / Public Areas** | | | | | | |
| L05-8200 | L5 - Final Paint @ Common / Public Areas | 3 | 3 | 24-Jun-14 | 26-Jun-14 | 0 |
| L05-8202 | L5 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 27-Jun-14 | 01-Jul-14 | 0 |
| L05-8204 | L5 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 27-Jun-14 | 01-Jul-14 | 0 |
| L05-8206 | L5 - Flooring @ Common / Public Areas | 3 | 3 | 01-Jul-14 | 03-Jul-14 | 0 |
| L05-8208 | L5 - Final Clean | 3 | 3 | 07-Jul-14 | 09-Jul-14 | 0 |
| L05-8210 | L5 - Owner Walk / Create Punchlist | 1 | 1 | 10-Jul-14 | 10-Jul-14 | 0 |
| L05-8212 | L5 - Final Punchlist | 5 | 5 | 11-Jul-14 | 17-Jul-14 | 0 |
| L05-8214 | L5 - Floor Complete | 0 | 0 | | 17-Jul-14 | 0 |
| **Level 6 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L06-8100 | L6 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 07-Apr-14 | 09-Apr-14 | 25 |
| L06-6026 | L6 - Pull Wire | 6 | 6 | 07-Apr-14 | 14-Apr-14 | 48 |
| L06-8102 | L6 - GWB Hang / Tape / Finish - (Including Common / | 14 | 14 | 15-May-14 | 04-Jun-14 | 0 |
| L06-8104 | L6 - Int Painting | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 0 |
| L06-8106 | L6 - Wallcoverings | 6 | 6 | 04-Jun-14 | 11-Jun-14 | 7 |
| L06-8108 | L6 - Elec Trim / Finish | 8 | 8 | 09-Jun-14 | 18-Jun-14 | 2 |
| L06-8110 | L6 - HVAC Trim / Finish | 8 | 8 | 09-Jun-14 | 18-Jun-14 | 2 |
| L06-8112 | L6 - Fire Sprinkler Trim / Finish | 8 | 8 | 09-Jun-14 | 18-Jun-14 | 2 |

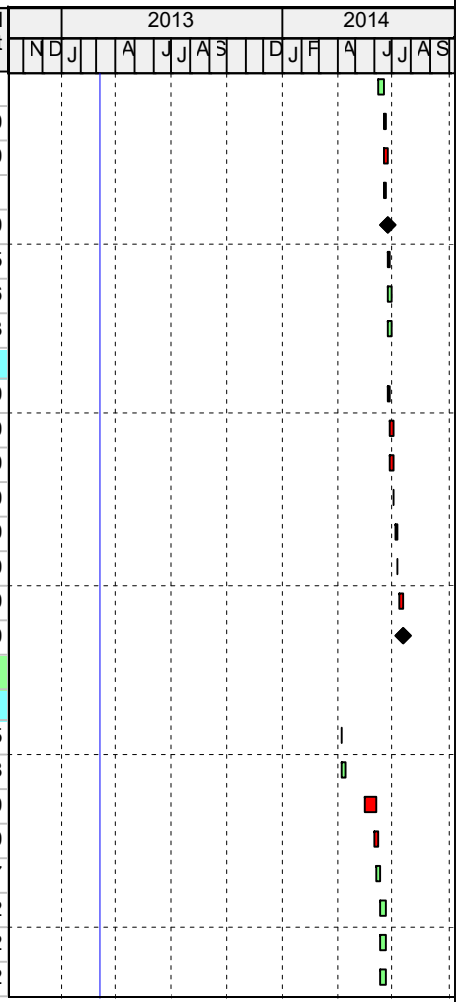



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8116 | L6 - Finish Carpentry / Millwork | 8 | 8 | 09-Jun-14 | 18-Jun-14 | 0 |
| L06-8118 | L6 - Elec Specialties Trim / Finish | 4 | 4 | 09-Jun-14 | 12-Jun-14 | 6 |
| L06-8120 | L6 - Ceramic Tile / Counter Tops | 8 | 8 | 11-Jun-14 | 20-Jun-14 | 0 |
| L06-8122 | L6 - Plumbing Trim / Finish | 8 | 8 | 13-Jun-14 | 24-Jun-14 | 1 |
| L06-8124 | L6 - Flooring @ Guest Rooms | 5 | 5 | 23-Jun-14 | 27-Jun-14 | 0 |
| L06-8126 | L6 - Doors & Hardware | 5 | 5 | 24-Jun-14 | 30-Jun-14 | 0 |
| L06-8128 | L6 - Bath Specialties / Tub Glazing | 3 | 3 | 25-Jun-14 | 27-Jun-14 | 1 |
| L06-8130 | L6 - Guest Rooms Substantially Complete | 0 | 0 | | 30-Jun-14 | 0 |
| L06-8114 | L6 - Signage | 3 | 3 | 01-Jul-14 | 03-Jul-14 | 5 |
| L06-8132 | L6 - Contractor Pre-Punchlist | 5 | 5 | 01-Jul-14 | 08-Jul-14 | 6 |
| L06-8134 | L6 - Pre-Clean | 5 | 5 | 01-Jul-14 | 08-Jul-14 | 3 |
| **Corridors / Common / Public Areas** | | | | | | |
| L06-8200 | L6 - Final Paint @ Common / Public Areas | 3 | 3 | 01-Jul-14 | 03-Jul-14 | 0 |
| L06-8202 | L6 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 07-Jul-14 | 09-Jul-14 | 0 |
| L06-8204 | L6 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 07-Jul-14 | 09-Jul-14 | 0 |
| L06-8206 | L6 - Flooring @ Common / Public Areas | 3 | 3 | 09-Jul-14 | 11-Jul-14 | 0 |
| L06-8208 | L6 - Final Clean | 3 | 3 | 14-Jul-14 | 16-Jul-14 | 0 |
| L06-8210 | L6 - Owner Walk / Create Punchlist | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 0 |
| L06-8212 | L6 - Final Punchlist | 5 | 5 | 18-Jul-14 | 24-Jul-14 | 0 |
| L06-8214 | L6 - Floor Complete | 0 | 0 | | 24-Jul-14 | 0 |
| **Level 7 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L07-8100 | L7 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 14-Apr-14 | 16-Apr-14 | 25 |
| L07-6026 | L7 - Pull Wire | 6 | 6 | 14-Apr-14 | 21-Apr-14 | 48 |
| L07-8102 | L7 - GWB Hang / Tape / Finish - (Including Common / | 14 | 14 | 22-May-14 | 11-Jun-14 | 0 |
| L07-8104 | L7 - Int Painting | 5 | 5 | 09-Jun-14 | 13-Jun-14 | 0 |
| L07-8106 | L7 - Wallcoverings | 6 | 6 | 11-Jun-14 | 18-Jun-14 | 7 |

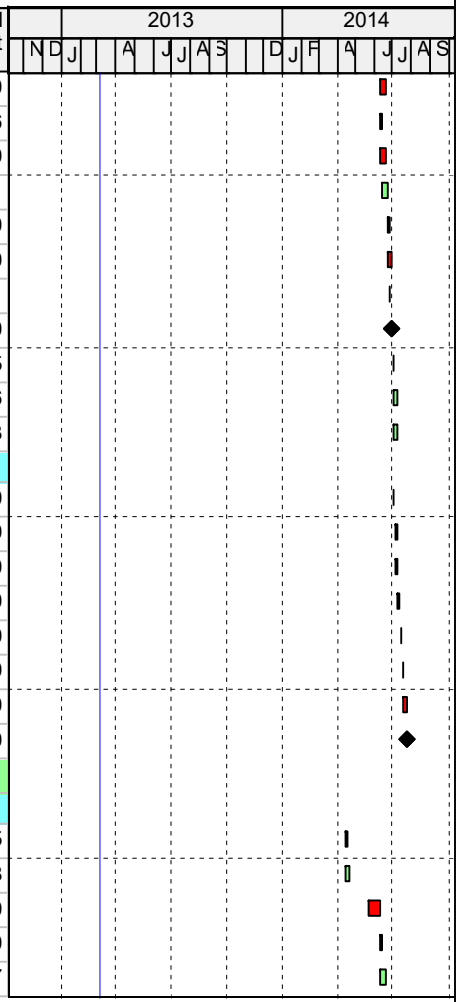



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8108 | L7 - Elec Trim / Finish | 8 | 8 | 16-Jun-14 | 25-Jun-14 | 2 |
| L07-8110 | L7 - HVAC Trim / Finish | 8 | 8 | 16-Jun-14 | 25-Jun-14 | 2 |
| L07-8112 | L7 - Fire Sprinkler Trim / Finish | 8 | 8 | 16-Jun-14 | 25-Jun-14 | 2 |
| L07-8116 | L7 - Finish Carpentry / Millwork | 8 | 8 | 16-Jun-14 | 25-Jun-14 | 0 |
| L07-8118 | L7 - Elec Specialties Trim / Finish | 4 | 4 | 16-Jun-14 | 19-Jun-14 | 6 |
| L07-8120 | L7 - Ceramic Tile / Counter Tops | 8 | 8 | 18-Jun-14 | 27-Jun-14 | 0 |
| L07-8122 | L7 - Plumbing Trim / Finish | 8 | 8 | 20-Jun-14 | 01-Jul-14 | 1 |
| L07-8124 | L7 - Flooring @ Guest Rooms | 5 | 5 | 30-Jun-14 | 07-Jul-14 | 0 |
| L07-8126 | L7 - Doors & Hardware | 5 | 5 | 01-Jul-14 | 08-Jul-14 | 0 |
| L07-8128 | L7 - Bath Specialties / Tub Glazing | 3 | 3 | 02-Jul-14 | 07-Jul-14 | 1 |
| L07-8130 | L7 - Guest Rooms Substantially Complete | 0 | 0 | | 08-Jul-14 | 0 |
| L07-8114 | L7 - Signage | 3 | 3 | 09-Jul-14 | 11-Jul-14 | 5 |
| L07-8132 | L7 - Contractor Pre-Punchlist | 5 | 5 | 09-Jul-14 | 15-Jul-14 | 6 |
| L07-8134 | L7 - Pre-Clean | 5 | 5 | 09-Jul-14 | 15-Jul-14 | 3 |
| **Corridors / Common / Public Areas** | | | | | | |
| L07-8200 | L7 - Final Paint @ Common / Public Areas | 3 | 3 | 09-Jul-14 | 11-Jul-14 | 0 |
| L07-8202 | L7 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 14-Jul-14 | 16-Jul-14 | 0 |
| L07-8204 | L7 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 14-Jul-14 | 16-Jul-14 | 0 |
| L07-8206 | L7 - Flooring @ Common / Public Areas | 3 | 3 | 16-Jul-14 | 18-Jul-14 | 0 |
| L07-8208 | L7 - Final Clean | 3 | 3 | 21-Jul-14 | 23-Jul-14 | 0 |
| L07-8210 | L7 - Owner Walk / Create Punchlist | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 0 |
| L07-8212 | L7 - Final Punchlist | 5 | 5 | 25-Jul-14 | 31-Jul-14 | 0 |
| L07-8214 | L7 - Floor Complete | 0 | 0 | | 31-Jul-14 | 0 |
| **Level 8 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L08-8100 | L8 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 21-Apr-14 | 23-Apr-14 | 25 |
| L08-6026 | L8 - Pull Wire | 6 | 6 | 21-Apr-14 | 28-Apr-14 | 48 |

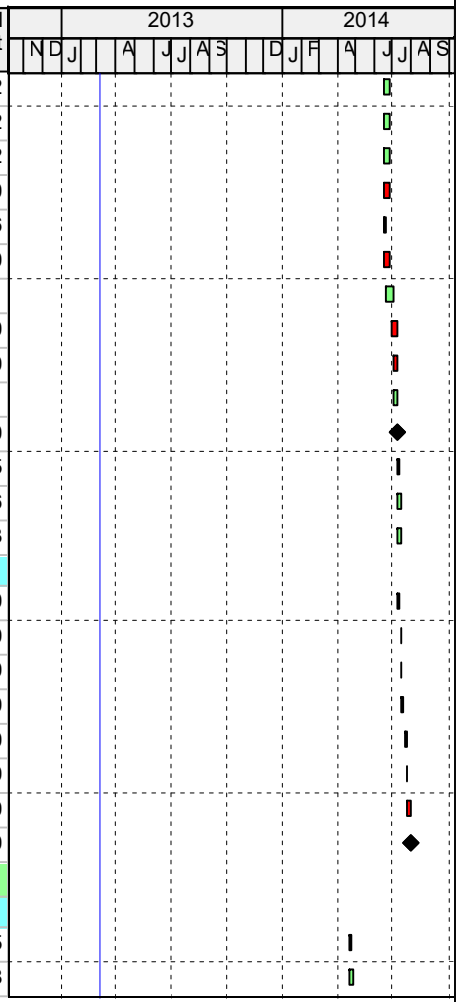



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8102 | L8 - GWB Hang / Tape / Finish - (Including Common / | 14 | 14 | 30-May-14 | 18-Jun-14 | 0 |
| L08-8104 | L8 - Int Painting | 5 | 5 | 16-Jun-14 | 20-Jun-14 | 0 |
| L08-8106 | L8 - Wallcoverings | 6 | 6 | 18-Jun-14 | 25-Jun-14 | 7 |
| L08-8108 | L8 - Elec Trim / Finish | 8 | 8 | 23-Jun-14 | 02-Jul-14 | 2 |
| L08-8110 | L8 - HVAC Trim / Finish | 8 | 8 | 23-Jun-14 | 02-Jul-14 | 2 |
| L08-8112 | L8 - Fire Sprinkler Trim / Finish | 8 | 8 | 23-Jun-14 | 02-Jul-14 | 2 |
| L08-8116 | L8 - Finish Carpentry / Millwork | 8 | 8 | 23-Jun-14 | 02-Jul-14 | 0 |
| L08-8118 | L8 - Elec Specialties Trim / Finish | 4 | 4 | 23-Jun-14 | 26-Jun-14 | 6 |
| L08-8120 | L8 - Ceramic Tile / Counter Tops | 8 | 8 | 25-Jun-14 | 07-Jul-14 | 0 |
| L08-8122 | L8 - Plumbing Trim / Finish | 8 | 8 | 27-Jun-14 | 09-Jul-14 | 1 |
| L08-8124 | L8 - Flooring @ Guest Rooms | 5 | 5 | 08-Jul-14 | 14-Jul-14 | 0 |
| L08-8126 | L8 - Doors & Hardware | 5 | 5 | 09-Jul-14 | 15-Jul-14 | 0 |
| L08-8128 | L8 - Bath Specialties / Tub Glazing | 3 | 3 | 10-Jul-14 | 14-Jul-14 | 1 |
| L08-8130 | L8 - Guest Rooms Substantially Complete | 0 | 0 | | 15-Jul-14 | 0 |
| L08-8114 | L8 - Signage | 3 | 3 | 16-Jul-14 | 18-Jul-14 | 5 |
| L08-8132 | L8 - Contractor Pre-Punchlist | 5 | 5 | 16-Jul-14 | 22-Jul-14 | 6 |
| L08-8134 | L8 - Pre-Clean | 5 | 5 | 16-Jul-14 | 22-Jul-14 | 3 |
| **Corridors / Common / Public Areas** | | | | | | |
| L08-8200 | L8 - Final Paint @ Common / Public Areas | 3 | 3 | 16-Jul-14 | 18-Jul-14 | 0 |
| L08-8202 | L8 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 21-Jul-14 | 23-Jul-14 | 0 |
| L08-8204 | L8 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 21-Jul-14 | 23-Jul-14 | 0 |
| L08-8206 | L8 - Flooring @ Common / Public Areas | 3 | 3 | 23-Jul-14 | 25-Jul-14 | 0 |
| L08-8208 | L8 - Final Clean | 3 | 3 | 28-Jul-14 | 30-Jul-14 | 0 |
| L08-8210 | L8 - Owner Walk / Create Punchlist | 1 | 1 | 31-Jul-14 | 31-Jul-14 | 0 |
| L08-8212 | L8 - Final Punchlist | 5 | 5 | 01-Aug-14 | 07-Aug-14 | 0 |
| L08-8214 | L8 - Floor Complete | 0 | 0 | | 07-Aug-14 | 0 |
| **Level 9 - (Guest Rooms)** | | | | | | |

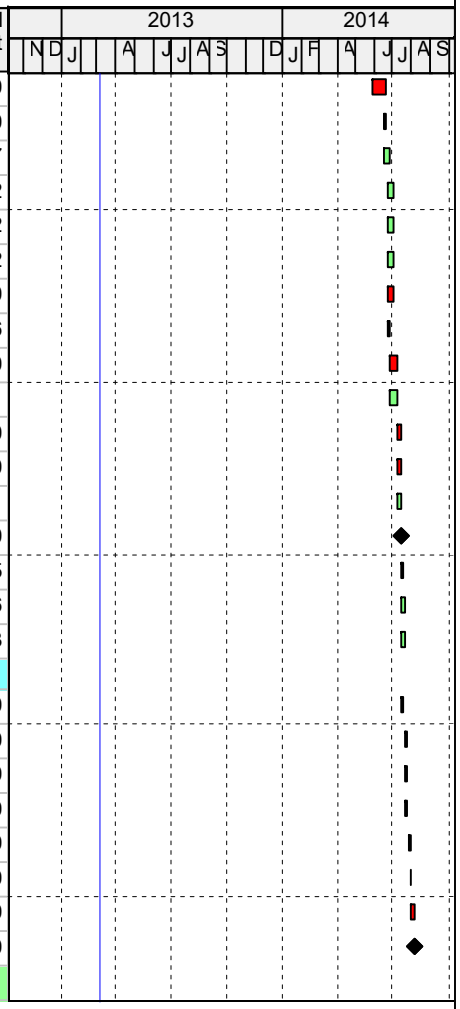



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Guest Rooms** | | | | | | |
| L09-8100 | L9 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 28-Apr-14 | 30-Apr-14 | 25 |
| L09-6026 | L9 - Pull Wire | 6 | 6 | 28-Apr-14 | 05-May-14 | 48 |
| L09-8102 | L9 - GWB Hang / Tape / Finish - (Including Common / | 14 | 14 | 06-Jun-14 | 25-Jun-14 | 0 |
| L09-8104 | L9 - Int Painting | 5 | 5 | 23-Jun-14 | 27-Jun-14 | 0 |
| L09-8106 | L9 - Wallcoverings | 6 | 6 | 25-Jun-14 | 02-Jul-14 | 7 |
| L09-8108 | L9 - Elec Trim / Finish | 8 | 8 | 30-Jun-14 | 10-Jul-14 | 2 |
| L09-8110 | L9 - HVAC Trim / Finish | 8 | 8 | 30-Jun-14 | 10-Jul-14 | 2 |
| L09-8112 | L9 - Fire Sprinkler Trim / Finish | 8 | 8 | 30-Jun-14 | 10-Jul-14 | 2 |
| L09-8116 | L9 - Finish Carpentry / Millwork | 8 | 8 | 30-Jun-14 | 10-Jul-14 | 0 |
| L09-8118 | L9 - Elec Specialties Trim / Finish | 4 | 4 | 30-Jun-14 | 03-Jul-14 | 6 |
| L09-8120 | L9 - Ceramic Tile / Counter Tops | 8 | 8 | 02-Jul-14 | 14-Jul-14 | 0 |
| L09-8122 | L9 - Plumbing Trim / Finish | 8 | 8 | 07-Jul-14 | 16-Jul-14 | 1 |
| L09-8124 | L9 - Flooring @ Guest Rooms | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 0 |
| L09-8126 | L9 - Doors & Hardware | 5 | 5 | 16-Jul-14 | 22-Jul-14 | 0 |
| L09-8128 | L9 - Bath Specialties / Tub Glazing | 3 | 3 | 17-Jul-14 | 21-Jul-14 | 1 |
| L09-8130 | L9 - Guest Rooms Substantially Complete | 0 | 0 | | 22-Jul-14 | 0 |
| L09-8114 | L9 - Signage | 3 | 3 | 23-Jul-14 | 25-Jul-14 | 5 |
| L09-8132 | L9 - Contractor Pre-Punchlist | 5 | 5 | 23-Jul-14 | 29-Jul-14 | 6 |
| L09-8134 | L9 - Pre-Clean | 5 | 5 | 23-Jul-14 | 29-Jul-14 | 3 |
| **Corridors / Common / Public Areas** | | | | | | |
| L09-8200 | L9 - Final Paint @ Common / Public Areas | 3 | 3 | 23-Jul-14 | 25-Jul-14 | 0 |
| L09-8202 | L9 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 28-Jul-14 | 30-Jul-14 | 0 |
| L09-8204 | L9 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 28-Jul-14 | 30-Jul-14 | 0 |
| L09-8206 | L9 - Flooring @ Common / Public Areas | 3 | 3 | 30-Jul-14 | 01-Aug-14 | 0 |
| L09-8208 | L9 - Final Clean | 3 | 3 | 04-Aug-14 | 06-Aug-14 | 0 |
| L09-8210 | L9 - Owner Walk / Create Punchlist | 1 | 1 | 07-Aug-14 | 07-Aug-14 | 0 |

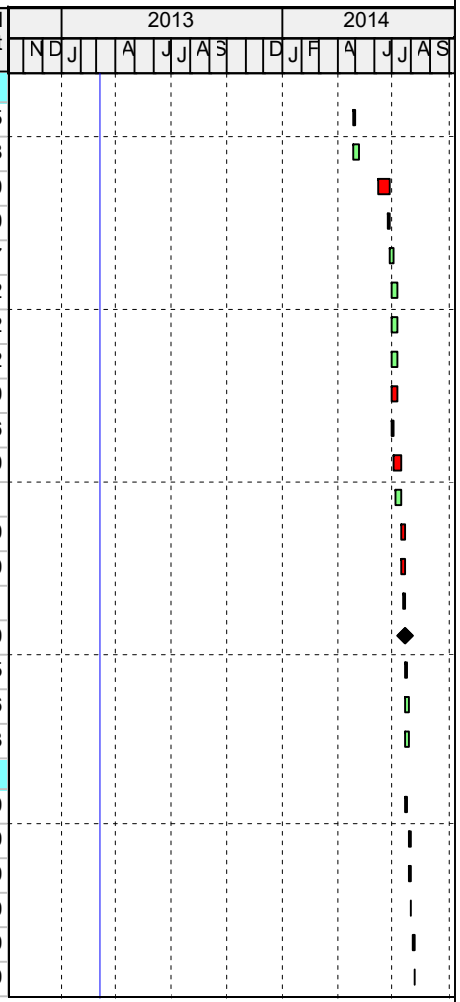



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8212 | L9 - Final Punchlist | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 0 |
| L09-8214 | L9 - Floor Complete | 0 | 0 | | 14-Aug-14 | 0 |
| **Level 10 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L10-8100 | L10 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 05-May-14 | 07-May-14 | 25 |
| L10-6026 | L10 - Pull Wire | 6 | 6 | 05-May-14 | 12-May-14 | 48 |
| L10-8102 | L10 - GWB Hang / Tape / Finish - (Including Commor | 14 | 14 | 13-Jun-14 | 02-Jul-14 | 0 |
| L10-8104 | L10 - Int Painting | 5 | 5 | 30-Jun-14 | 07-Jul-14 | 0 |
| L10-8106 | L10 - Wallcoverings | 6 | 6 | 02-Jul-14 | 10-Jul-14 | 7 |
| L10-8108 | L10 - Elec Trim / Finish | 8 | 8 | 08-Jul-14 | 17-Jul-14 | 2 |
| L10-8110 | L10 - HVAC Trim / Finish | 8 | 8 | 08-Jul-14 | 17-Jul-14 | 2 |
| L10-8112 | L10 - Fire Sprinkler Trim / Finish | 8 | 8 | 08-Jul-14 | 17-Jul-14 | 2 |
| L10-8116 | L10 - Finish Carpentry / Millwork | 8 | 8 | 08-Jul-14 | 17-Jul-14 | 0 |
| L10-8118 | L10 - Elec Specialties Trim / Finish | 4 | 4 | 08-Jul-14 | 11-Jul-14 | 6 |
| L10-8120 | L10 - Ceramic Tile / Counter Tops | 8 | 8 | 10-Jul-14 | 21-Jul-14 | 0 |
| L10-8122 | L10 - Plumbing Trim / Finish | 8 | 8 | 14-Jul-14 | 23-Jul-14 | 1 |
| L10-8124 | L10 - Flooring @ Guest Rooms | 5 | 5 | 22-Jul-14 | 28-Jul-14 | 0 |
| L10-8126 | L10 - Doors & Hardware | 5 | 5 | 23-Jul-14 | 29-Jul-14 | 0 |
| L10-8128 | L10 - Bath Specialties / Tub Glazing | 3 | 3 | 24-Jul-14 | 28-Jul-14 | 1 |
| L10-8130 | L10 - Guest Rooms Substantially Complete | 0 | 0 | | 29-Jul-14 | 0 |
| L10-8114 | L10 - Signage | 3 | 3 | 30-Jul-14 | 01-Aug-14 | 5 |
| L10-8132 | L10 - Contractor Pre-Punchlist | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 6 |
| L10-8134 | L10 - Pre-Clean | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 3 |
| **Corridors / Common / Public Areas** | | | | | | |
| L10-8200 | L10 - Final Paint @ Common / Public Areas | 3 | 3 | 30-Jul-14 | 01-Aug-14 | 0 |
| L10-8202 | L10 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 04-Aug-14 | 06-Aug-14 | 0 |
| L10-8204 | L10 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 04-Aug-14 | 06-Aug-14 | 0 |

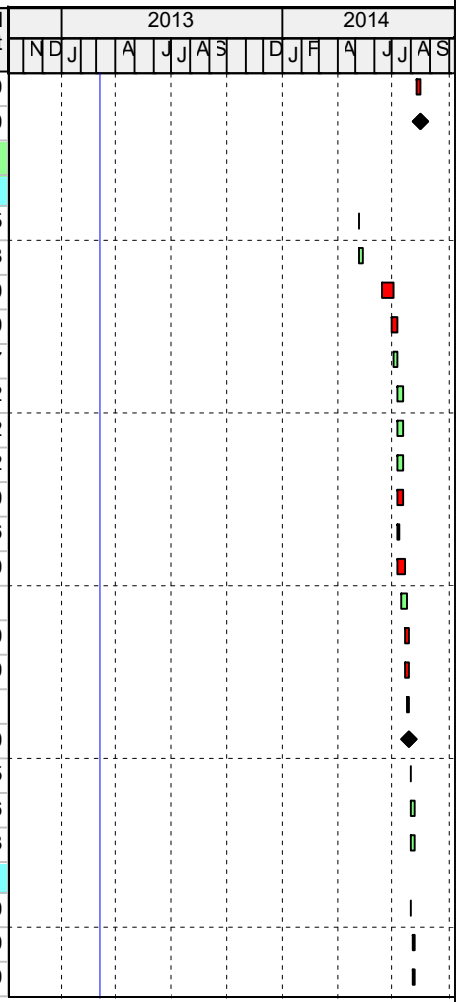



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8206 | L10 - Flooring @ Common / Public Areas | 3 | 3 | 06-Aug-14 | 08-Aug-14 | 0 |
| L10-8208 | L10 - Final Clean | 3 | 3 | 11-Aug-14 | 13-Aug-14 | 0 |
| L10-8210 | L10 - Owner Walk / Create Punchlist | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 0 |
| L10-8212 | L10 - Final Punchlist | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 0 |
| L10-8214 | L10 - Floor Complete | 0 | 0 | | 21-Aug-14 | 0 |
| **Level 11 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L11-8100 | L11 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 12-May-14 | 14-May-14 | 25 |
| L11-6026 | L11 - Pull Wire | 6 | 6 | 12-May-14 | 19-May-14 | 48 |
| L11-8102 | L11 - GWB Hang / Tape / Finish - (Including Common | 14 | 14 | 20-Jun-14 | 10-Jul-14 | 0 |
| L11-8104 | L11 - Int Painting | 5 | 5 | 08-Jul-14 | 14-Jul-14 | 0 |
| L11-8106 | L11 - Wallcoverings | 6 | 6 | 10-Jul-14 | 17-Jul-14 | 7 |
| L11-8108 | L11 - Elec Trim / Finish | 8 | 8 | 15-Jul-14 | 24-Jul-14 | 2 |
| L11-8110 | L11 - HVAC Trim / Finish | 8 | 8 | 15-Jul-14 | 24-Jul-14 | 2 |
| L11-8112 | L11 - Fire Sprinkler Trim / Finish | 8 | 8 | 15-Jul-14 | 24-Jul-14 | 2 |
| L11-8116 | L11 - Finish Carpentry / Millwork | 8 | 8 | 15-Jul-14 | 24-Jul-14 | 0 |
| L11-8118 | L11 - Elec Specialties Trim / Finish | 4 | 4 | 15-Jul-14 | 18-Jul-14 | 6 |
| L11-8120 | L11 - Ceramic Tile / Counter Tops | 8 | 8 | 17-Jul-14 | 28-Jul-14 | 0 |
| L11-8122 | L11 - Plumbing Trim / Finish | 8 | 8 | 21-Jul-14 | 30-Jul-14 | 1 |
| L11-8124 | L11 - Flooring @ Guest Rooms | 5 | 5 | 29-Jul-14 | 04-Aug-14 | 0 |
| L11-8126 | L11 - Doors & Hardware | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 0 |
| L11-8128 | L11 - Bath Specialties / Tub Glazing | 3 | 3 | 31-Jul-14 | 04-Aug-14 | 1 |
| L11-8130 | L11 - Guest Rooms Substantially Complete | 0 | 0 | | 05-Aug-14 | 0 |
| L11-8114 | L11 - Signage | 3 | 3 | 06-Aug-14 | 08-Aug-14 | 5 |
| L11-8132 | L11 - Contractor Pre-Punchlist | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 6 |
| L11-8134 | L11 - Pre-Clean | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 3 |
| **Corridors / Common / Public Areas** | | | | | | |

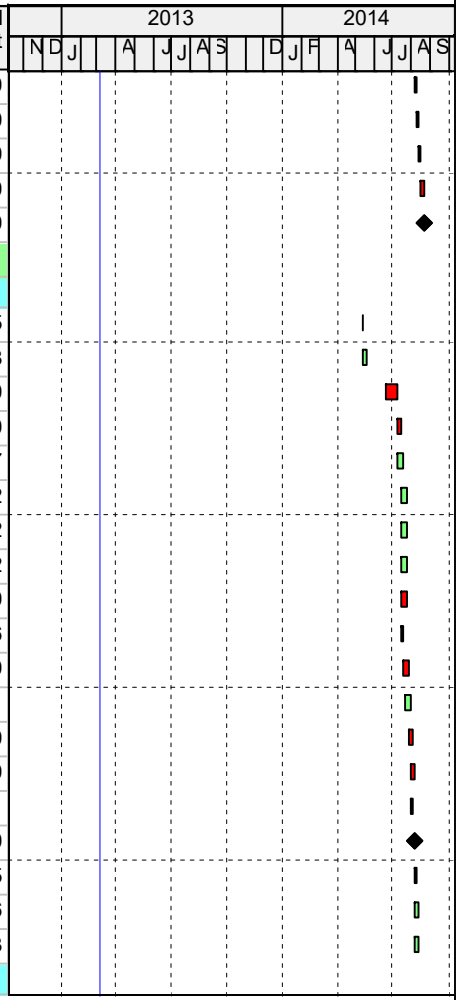



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8200 | L11 - Final Paint @ Common / Public Areas | 3 | 3 | 06-Aug-14 | 08-Aug-14 | 0 |
| L11-8202 | L11 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 11-Aug-14 | 13-Aug-14 | 0 |
| L11-8204 | L11 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 11-Aug-14 | 13-Aug-14 | 0 |
| L11-8206 | L11 - Flooring @ Common / Public Areas | 3 | 3 | 13-Aug-14 | 15-Aug-14 | 0 |
| L11-8208 | L11 - Final Clean | 3 | 3 | 18-Aug-14 | 20-Aug-14 | 0 |
| L11-8210 | L11 - Owner Walk / Create Punchlist | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 0 |
| L11-8212 | L11 - Final Punchlist | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 0 |
| L11-8214 | L11 - Floor Complete | 0 | 0 | | 28-Aug-14 | 0 |
| **Level 12 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L12-8100 | L12 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 19-May-14 | 21-May-14 | 25 |
| L12-6026 | L12 - Pull Wire | 6 | 6 | 19-May-14 | 27-May-14 | 48 |
| L12-8102 | L12 - GWB Hang / Tape / Finish - (Including Commor | 14 | 14 | 27-Jun-14 | 17-Jul-14 | 0 |
| L12-8104 | L12 - Int Painting | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 0 |
| L12-8106 | L12 - Wallcoverings | 6 | 6 | 17-Jul-14 | 24-Jul-14 | 7 |
| L12-8108 | L12 - Elec Trim / Finish | 8 | 8 | 22-Jul-14 | 31-Jul-14 | 2 |
| L12-8110 | L12 - HVAC Trim / Finish | 8 | 8 | 22-Jul-14 | 31-Jul-14 | 2 |
| L12-8112 | L12 - Fire Sprinkler Trim / Finish | 8 | 8 | 22-Jul-14 | 31-Jul-14 | 2 |
| L12-8116 | L12 - Finish Carpentry / Millwork | 8 | 8 | 22-Jul-14 | 31-Jul-14 | 0 |
| L12-8118 | L12 - Elec Specialties Trim / Finish | 4 | 4 | 22-Jul-14 | 25-Jul-14 | 6 |
| L12-8120 | L12 - Ceramic Tile / Counter Tops | 8 | 8 | 24-Jul-14 | 04-Aug-14 | 0 |
| L12-8122 | L12 - Plumbing Trim / Finish | 8 | 8 | 28-Jul-14 | 06-Aug-14 | 1 |
| L12-8124 | L12 - Flooring @ Guest Rooms | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 0 |
| L12-8126 | L12 - Doors & Hardware | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 0 |
| L12-8128 | L12 - Bath Specialties / Tub Glazing | 3 | 3 | 07-Aug-14 | 11-Aug-14 | 1 |
| L12-8130 | L12 - Guest Rooms Substantially Complete | 0 | 0 | | 12-Aug-14 | 0 |
| L12-8114 | L12 - Signage | 3 | 3 | 13-Aug-14 | 15-Aug-14 | 5 |

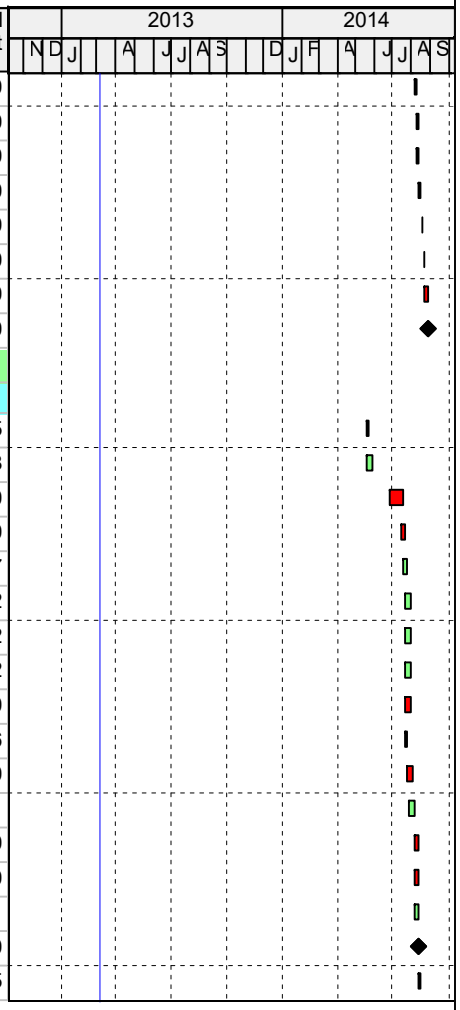



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8132 | L12 - Contractor Pre-Punchlist | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 6 |
| L12-8134 | L12 - Pre-Clean | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 3 |
| **Corridors / Common / Public Areas** | | | | | | |
| L12-8200 | L12 - Final Paint @ Common / Public Areas | 3 | 3 | 13-Aug-14 | 15-Aug-14 | 0 |
| L12-8202 | L12 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 18-Aug-14 | 20-Aug-14 | 0 |
| L12-8204 | L12 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 18-Aug-14 | 20-Aug-14 | 0 |
| L12-8206 | L12 - Flooring @ Common / Public Areas | 3 | 3 | 20-Aug-14 | 22-Aug-14 | 0 |
| L12-8208 | L12 - Final Clean | 3 | 3 | 25-Aug-14 | 27-Aug-14 | 0 |
| L12-8210 | L12 - Owner Walk / Create Punchlist | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 0 |
| L12-8212 | L12 - Final Punchlist | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 0 |
| L12-8214 | L12 - Floor Complete | 0 | 0 | | 05-Sep-14 | 0 |
| **Level 14 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L14-8100 | L14 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 27-May-14 | 29-May-14 | 25 |
| L14-6026 | L14 - Pull Wire | 6 | 6 | 27-May-14 | 03-Jun-14 | 48 |
| L14-8102 | L14 - GWB Hang / Tape / Finish - (Including Commor | 14 | 14 | 07-Jul-14 | 24-Jul-14 | 0 |
| L14-8104 | L14 - Int Painting | 5 | 5 | 22-Jul-14 | 28-Jul-14 | 0 |
| L14-8106 | L14 - Wallcoverings | 6 | 6 | 24-Jul-14 | 31-Jul-14 | 7 |
| L14-8108 | L14 - Elec Trim / Finish | 8 | 8 | 29-Jul-14 | 07-Aug-14 | 2 |
| L14-8110 | L14 - HVAC Trim / Finish | 8 | 8 | 29-Jul-14 | 07-Aug-14 | 2 |
| L14-8112 | L14 - Fire Sprinkler Trim / Finish | 8 | 8 | 29-Jul-14 | 07-Aug-14 | 2 |
| L14-8116 | L14 - Finish Carpentry / Millwork | 8 | 8 | 29-Jul-14 | 07-Aug-14 | 0 |
| L14-8118 | L14 - Elec Specialties Trim / Finish | 4 | 4 | 29-Jul-14 | 01-Aug-14 | 6 |
| L14-8120 | L14 - Ceramic Tile / Counter Tops | 8 | 8 | 31-Jul-14 | 11-Aug-14 | 0 |
| L14-8122 | L14 - Plumbing Trim / Finish | 8 | 8 | 04-Aug-14 | 13-Aug-14 | 1 |
| L14-8124 | L14 - Flooring @ Guest Rooms | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 0 |
| L14-8126 | L14 - Doors & Hardware | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 0 |

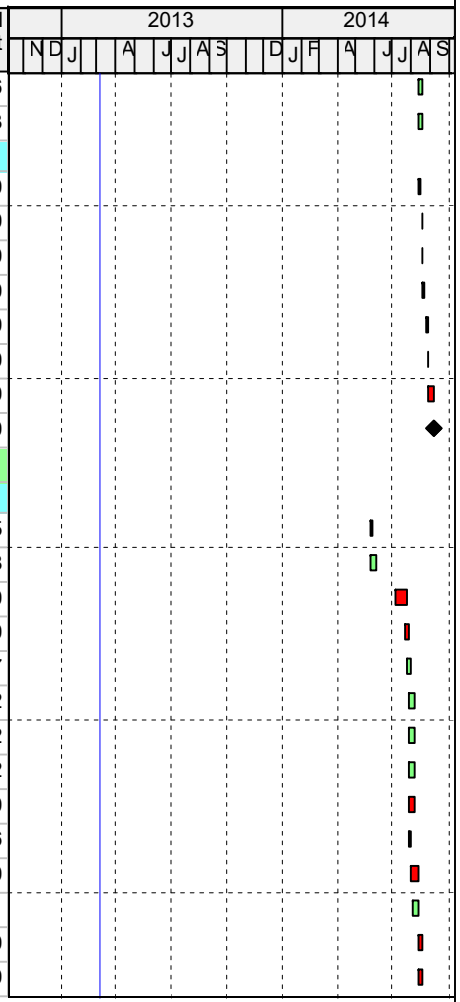



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8128 | L14 - Bath Specialties / Tub Glazing | 3 | 3 | 14-Aug-14 | 18-Aug-14 | 1 |
| L14-8130 | L14 - Guest Rooms Substantially Complete | 0 | 0 | | 19-Aug-14 | 0 |
| L14-8114 | L14 - Signage | 3 | 3 | 20-Aug-14 | 22-Aug-14 | 5 |
| L14-8132 | L14 - Contractor Pre-Punchlist | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 6 |
| L14-8134 | L14 - Pre-Clean | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 3 |
| **Corridors / Common / Public Areas** | | | | | | |
| L14-8200 | L14 - Final Paint @ Common / Public Areas | 3 | 3 | 20-Aug-14 | 22-Aug-14 | 0 |
| L14-8202 | L14 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 25-Aug-14 | 27-Aug-14 | 0 |
| L14-8204 | L14 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 25-Aug-14 | 27-Aug-14 | 0 |
| L14-8206 | L14 - Flooring @ Common / Public Areas | 3 | 3 | 27-Aug-14 | 29-Aug-14 | 0 |
| L14-8208 | L14 - Final Clean | 3 | 3 | 02-Sep-14 | 04-Sep-14 | 0 |
| L14-8210 | L14 - Owner Walk / Create Punchlist | 1 | 1 | 05-Sep-14 | 05-Sep-14 | 0 |
| L14-8212 | L14 - Final Punchlist | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 0 |
| L14-8214 | L14 - Floor Complete | 0 | 0 | | 12-Sep-14 | 0 |
| **Level 15 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L15-8100 | L15 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 03-Jun-14 | 05-Jun-14 | 25 |
| L15-6026 | L15 - Pull Wire | 6 | 6 | 03-Jun-14 | 10-Jun-14 | 48 |
| L15-8102 | L15 - GWB Hang / Tape / Finish - (Including Commor | 14 | 14 | 14-Jul-14 | 31-Jul-14 | 0 |
| L15-8104 | L15 - Int Painting | 5 | 5 | 29-Jul-14 | 04-Aug-14 | 0 |
| L15-8106 | L15 - Wallcoverings | 6 | 6 | 31-Jul-14 | 07-Aug-14 | 7 |
| L15-8108 | L15 - Elec Trim / Finish | 8 | 8 | 05-Aug-14 | 14-Aug-14 | 2 |
| L15-8110 | L15 - HVAC Trim / Finish | 8 | 8 | 05-Aug-14 | 14-Aug-14 | 2 |
| L15-8112 | L15 - Fire Sprinkler Trim / Finish | 8 | 8 | 05-Aug-14 | 14-Aug-14 | 2 |
| L15-8116 | L15 - Finish Carpentry / Millwork | 8 | 8 | 05-Aug-14 | 14-Aug-14 | 0 |
| L15-8118 | L15 - Elec Specialties Trim / Finish | 4 | 4 | 05-Aug-14 | 08-Aug-14 | 6 |
| L15-8120 | L15 - Ceramic Tile / Counter Tops | 8 | 8 | 07-Aug-14 | 18-Aug-14 | 0 |

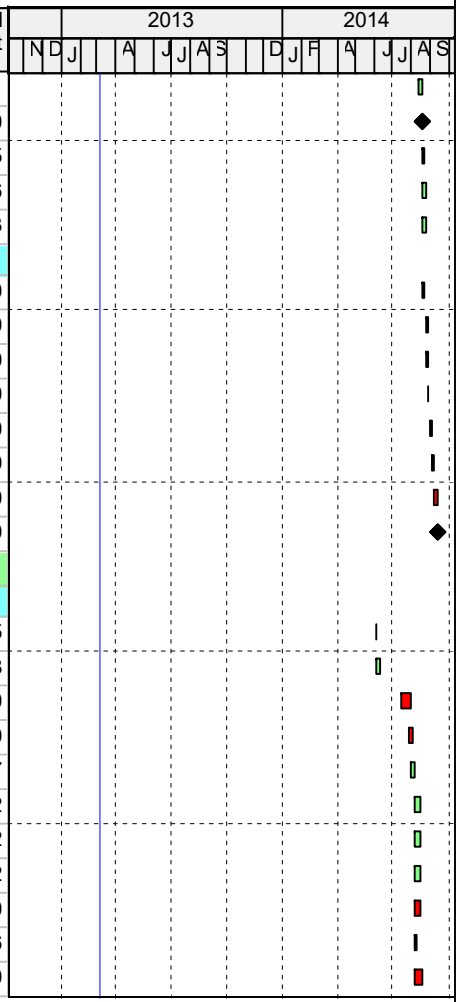



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8122 | L15 - Plumbing Trim / Finish | 8 | 8 | 11-Aug-14 | 20-Aug-14 | 1 |
| L15-8124 | L15 - Flooring @ Guest Rooms | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 0 |
| L15-8126 | L15 - Doors & Hardware | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 0 |
| L15-8128 | L15 - Bath Specialties / Tub Glazing | 3 | 3 | 21-Aug-14 | 25-Aug-14 | 1 |
| L15-8130 | L15 - Guest Rooms Substantially Complete | 0 | 0 | | 26-Aug-14 | 0 |
| L15-8114 | L15 - Signage | 3 | 3 | 27-Aug-14 | 29-Aug-14 | 5 |
| L15-8132 | L15 - Contractor Pre-Punchlist | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 6 |
| L15-8134 | L15 - Pre-Clean | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 3 |
| **Corridors / Common / Public Areas** | | | | | | |
| L15-8200 | L15 - Final Paint @ Common / Public Areas | 3 | 3 | 27-Aug-14 | 29-Aug-14 | 0 |
| L15-8202 | L15 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 02-Sep-14 | 04-Sep-14 | 0 |
| L15-8204 | L15 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 02-Sep-14 | 04-Sep-14 | 0 |
| L15-8206 | L15 - Flooring @ Common / Public Areas | 3 | 3 | 04-Sep-14 | 08-Sep-14 | 0 |
| L15-8208 | L15 - Final Clean | 3 | 3 | 09-Sep-14 | 11-Sep-14 | 0 |
| L15-8210 | L15 - Owner Walk / Create Punchlist | 1 | 1 | 12-Sep-14 | 12-Sep-14 | 0 |
| L15-8212 | L15 - Final Punchlist | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 0 |
| L15-8214 | L15 - Floor Complete | 0 | 0 | | 19-Sep-14 | 0 |
| **Level 16 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L16-8100 | L16 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 10-Jun-14 | 12-Jun-14 | 25 |
| L16-6026 | L16 - Pull Wire | 6 | 6 | 10-Jun-14 | 17-Jun-14 | 48 |
| L16-8102 | L16 - GWB Hang / Tape / Finish - (Including Commor | 14 | 14 | 21-Jul-14 | 07-Aug-14 | 0 |
| L16-8104 | L16 - Int Painting | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 0 |
| L16-8106 | L16 - Wallcoverings | 6 | 6 | 07-Aug-14 | 14-Aug-14 | 7 |
| L16-8108 | L16 - Elec Trim / Finish | 8 | 8 | 12-Aug-14 | 21-Aug-14 | 2 |
| L16-8110 | L16 - HVAC Trim / Finish | 8 | 8 | 12-Aug-14 | 21-Aug-14 | 2 |
| L16-8112 | L16 - Fire Sprinkler Trim / Finish | 8 | 8 | 12-Aug-14 | 21-Aug-14 | 2 |

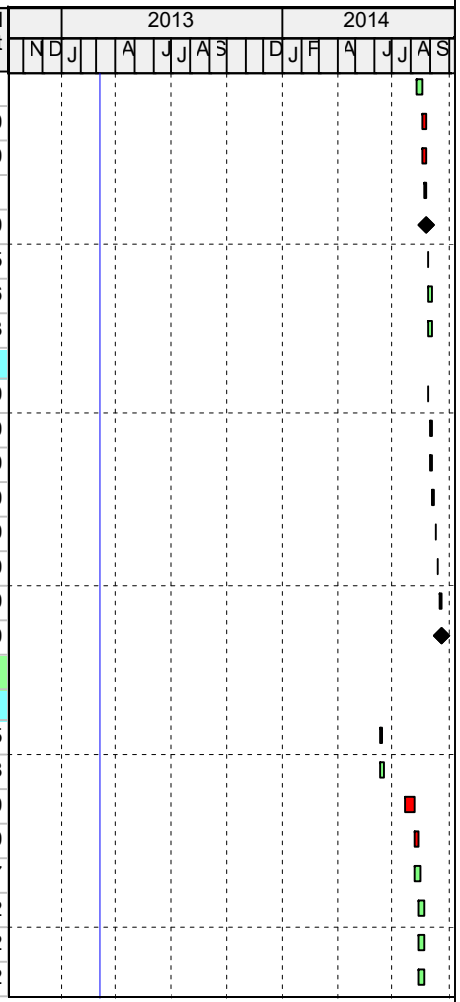



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8116 | L16 - Finish Carpentry / Millwork | 8 | 8 | 12-Aug-14 | 21-Aug-14 | 0 |
| L16-8118 | L16 - Elec Specialties Trim / Finish | 4 | 4 | 12-Aug-14 | 15-Aug-14 | 6 |
| L16-8120 | L16 - Ceramic Tile / Counter Tops | 8 | 8 | 14-Aug-14 | 25-Aug-14 | 0 |
| L16-8122 | L16 - Plumbing Trim / Finish | 8 | 8 | 18-Aug-14 | 27-Aug-14 | 1 |
| L16-8124 | L16 - Flooring @ Guest Rooms | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 0 |
| L16-8126 | L16 - Doors & Hardware | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 0 |
| L16-8128 | L16 - Bath Specialties / Tub Glazing | 3 | 3 | 28-Aug-14 | 02-Sep-14 | 1 |
| L16-8130 | L16 - Guest Rooms Substantially Complete | 0 | 0 | | 03-Sep-14 | 0 |
| L16-8114 | L16 - Signage | 3 | 3 | 04-Sep-14 | 08-Sep-14 | 5 |
| L16-8132 | L16 - Contractor Pre-Punchlist | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 6 |
| L16-8134 | L16 - Pre-Clean | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 3 |
| **Corridors / Common / Public Areas** | | | | | | |
| L16-8200 | L16 - Final Paint @ Common / Public Areas | 3 | 3 | 04-Sep-14 | 08-Sep-14 | 0 |
| L16-8202 | L16 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 09-Sep-14 | 11-Sep-14 | 0 |
| L16-8204 | L16 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 09-Sep-14 | 11-Sep-14 | 0 |
| L16-8206 | L16 - Flooring @ Common / Public Areas | 3 | 3 | 11-Sep-14 | 15-Sep-14 | 0 |
| L16-8208 | L16 - Final Clean | 3 | 3 | 16-Sep-14 | 18-Sep-14 | 0 |
| L16-8210 | L16 - Owner Walk / Create Punchlist | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 0 |
| L16-8212 | L16 - Final Punchlist | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 0 |
| L16-8214 | L16 - Floor Complete | 0 | 0 | | 26-Sep-14 | 0 |
| **Level 17 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L17-8100 | L17 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 17-Jun-14 | 19-Jun-14 | 25 |
| L17-6026 | L17 - Pull Wire | 6 | 6 | 17-Jun-14 | 24-Jun-14 | 48 |
| L17-8102 | L17 - GWB Hang / Tape / Finish - (Including Commor | 14 | 14 | 28-Jul-14 | 14-Aug-14 | 0 |
| L17-8104 | L17 - Int Painting | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 0 |
| L17-8106 | L17 - Wallcoverings | 6 | 6 | 14-Aug-14 | 21-Aug-14 | 7 |

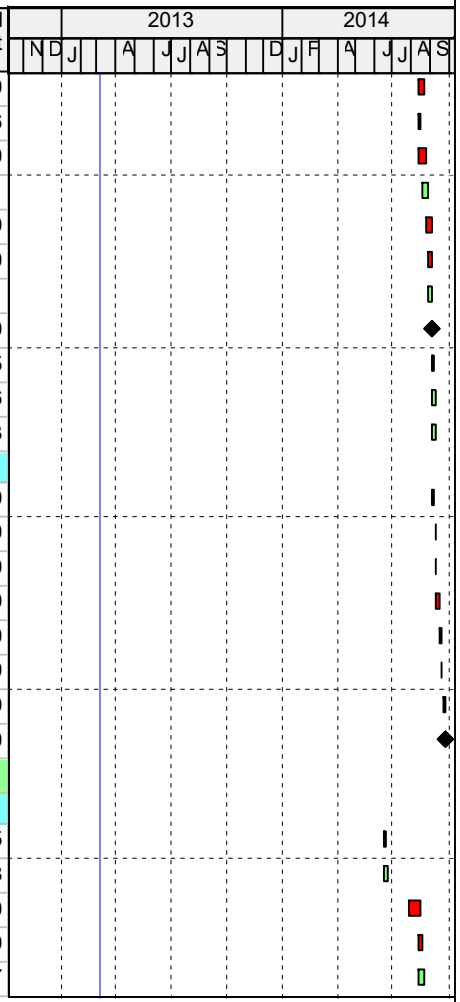



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8108 | L17 - Elec Trim / Finish | 8 | 8 | 19-Aug-14 | 28-Aug-14 | 2 |
| L17-8110 | L17 - HVAC Trim / Finish | 8 | 8 | 19-Aug-14 | 28-Aug-14 | 2 |
| L17-8112 | L17 - Fire Sprinkler Trim / Finish | 8 | 8 | 19-Aug-14 | 28-Aug-14 | 2 |
| L17-8116 | L17 - Finish Carpentry / Millwork | 8 | 8 | 19-Aug-14 | 28-Aug-14 | 0 |
| L17-8118 | L17 - Elec Specialties Trim / Finish | 4 | 4 | 19-Aug-14 | 22-Aug-14 | 6 |
| L17-8120 | L17 - Ceramic Tile / Counter Tops | 8 | 8 | 21-Aug-14 | 02-Sep-14 | 0 |
| L17-8122 | L17 - Plumbing Trim / Finish | 8 | 8 | 25-Aug-14 | 04-Sep-14 | 1 |
| L17-8124 | L17 - Flooring @ Guest Rooms | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 0 |
| L17-8126 | L17 - Doors & Hardware | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 0 |
| L17-8128 | L17 - Bath Specialties / Tub Glazing | 3 | 3 | 05-Sep-14 | 09-Sep-14 | 1 |
| L17-8130 | L17 - Guest Rooms Substantially Complete | 0 | 0 | | 10-Sep-14 | 0 |
| L17-8114 | L17 - Signage | 3 | 3 | 11-Sep-14 | 15-Sep-14 | 5 |
| L17-8132 | L17 - Contractor Pre-Punchlist | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 6 |
| L17-8134 | L17 - Pre-Clean | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 3 |
| **Corridors / Common / Public Areas** | | | | | | |
| L17-8200 | L17 - Final Paint @ Common / Public Areas | 3 | 3 | 11-Sep-14 | 15-Sep-14 | 0 |
| L17-8202 | L17 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 16-Sep-14 | 18-Sep-14 | 0 |
| L17-8204 | L17 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 16-Sep-14 | 18-Sep-14 | 0 |
| L17-8206 | L17 - Flooring @ Common / Public Areas | 3 | 3 | 18-Sep-14 | 22-Sep-14 | 0 |
| L17-8208 | L17 - Final Clean | 3 | 3 | 23-Sep-14 | 25-Sep-14 | 0 |
| L17-8210 | L17 - Owner Walk / Create Punchlist | 1 | 1 | 26-Sep-14 | 26-Sep-14 | 0 |
| L17-8212 | L17 - Final Punchlist | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 0 |
| L17-8214 | L17 - Floor Complete | 0 | 0 | | 03-Oct-14 | 0 |
| **Finishes @ Man Lifts Hold Outs - (All Floors)** | | | | | | |
| HO-8450 | HoldOut - Insulation / Slab Edge Fire Proofing | 3 | 3 | 04-Aug-14 | 06-Aug-14 | 26 |
| HO-8452 | HoldOut - GWB Hang / Tape / Finish | 10 | 10 | 05-Aug-14 | 18-Aug-14 | 26 |
| HO-8454 | HoldOut - Int Painting | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 26 |

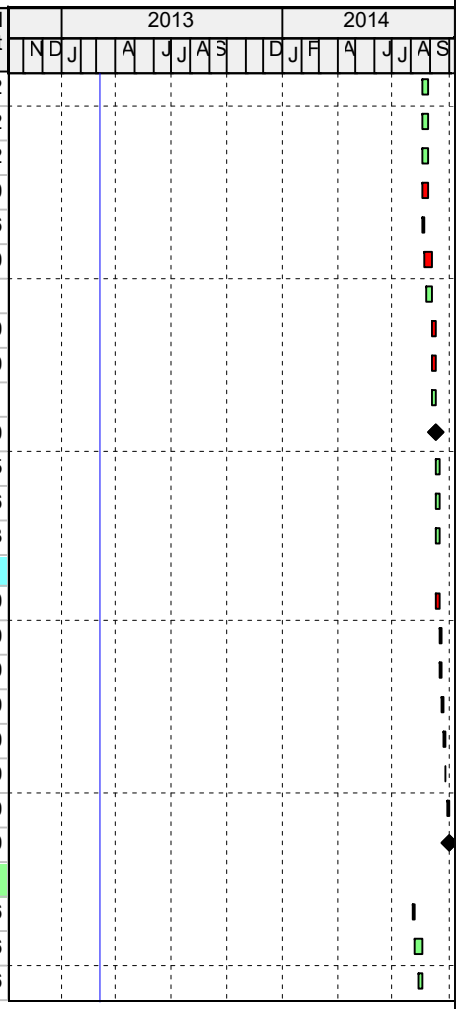



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| HO-8456 | HoldOut - Flooring | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 26 |
| HO-8458 | HoldOut - Final Clean | 3 | 3 | 19-Aug-14 | 21-Aug-14 | 26 |
| HO-8460 | HoldOut - Final Punchlist | 3 | 3 | 22-Aug-14 | 26-Aug-14 | 26 |
| **Mech Penthouse** | | | | | | |
| PH-6026 | PH - Pull Wire | 5 | 5 | 17-Jun-14 | 23-Jun-14 | 54 |
| PH-8100 | PH - Insulation | 3 | 3 | 18-Jun-14 | 20-Jun-14 | 34 |
| PH-8102 | PH - GWB Hang / Tape / Finish - (Including Common | 10 | 10 | 28-Jul-14 | 08-Aug-14 | 10 |
| PH-8104 | PH - Int Painting | 4 | 4 | 06-Aug-14 | 11-Aug-14 | 10 |
| PH-8108 | PH - Elec Trim / Finish | 10 | 10 | 12-Aug-14 | 25-Aug-14 | 10 |
| PH-8110 | PH - HVAC Trim / Finish | 10 | 10 | 12-Aug-14 | 25-Aug-14 | 10 |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 15 |
| PH-8114 | PH - Signage | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 26 |
| PH-8118 | PH - Elec Specialties Trim / Finish | 4 | 4 | 12-Aug-14 | 15-Aug-14 | 16 |
| PH-8116 | PH - Finish Carpentry / Millwork | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 14 |
| PH-8122 | PH - Plumbing Trim / Finish | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 15 |
| PH-8124 | PH - Flooring | 4 | 4 | 26-Aug-14 | 29-Aug-14 | 10 |
| PH-8126 | PH - Doors & Hardware | 3 | 3 | 28-Aug-14 | 02-Sep-14 | 10 |
| PH-8130 | PH - Guest Rooms Substantially Complete | 0 | 0 | | 02-Sep-14 | 10 |
| PH-8132 | PH - Contractor Pre-Punchlist | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 11 |
| PH-8134 | PH - Pre-Clean | 3 | 3 | 03-Sep-14 | 05-Sep-14 | 10 |
| PH-8208 | PH - Final Clean | 3 | 3 | 08-Sep-14 | 10-Sep-14 | 10 |
| PH-8210 | PH - Owner Walk / Create Punchlist | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 10 |
| PH-8212 | PH - Final Punchlist | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 10 |
| PH-8214 | PH - Floor Complete | 0 | 0 | | 18-Sep-14 | 10 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| **Smoke Control** | | | | | | |
| CO-7104 | Smoke Control Pre-Testing | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 3 |

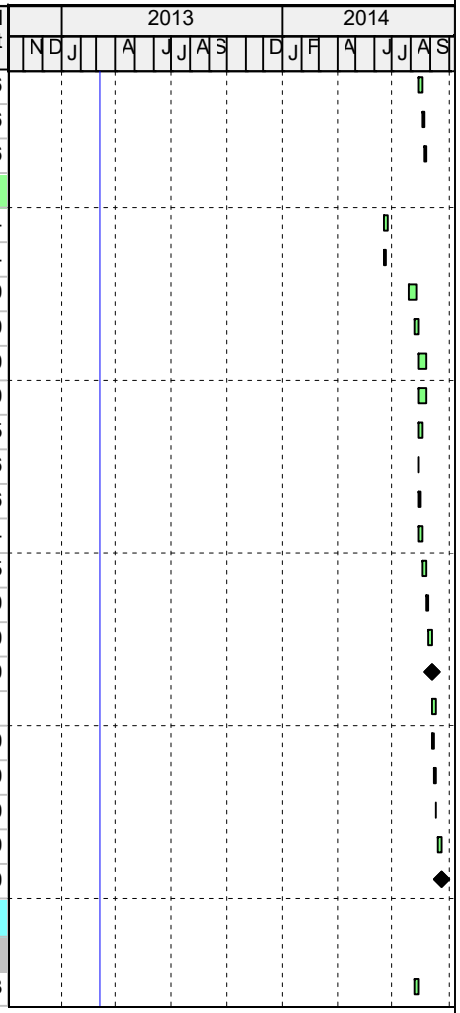


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7106 | City of Bellevue Smoke Control Testing | 3 | 3 | 13-Aug-14 | 15-Aug-14 | 3 |
| CO-7108 | Final Marriott Smoke Control Testing | 2 | 2 | 18-Aug-14 | 19-Aug-14 | 3 |
| **Fire Sprinklers** | | | | | | |
| CO-7110 | Fire Sprinkler Pre-Testing | 3 | 3 | 06-Aug-14 | 08-Aug-14 | 4 |
| CO-7112 | City of Bellevue Fire Sprinkler Inspection / Approval | 3 | 3 | 11-Aug-14 | 13-Aug-14 | 4 |
| CO-7114 | Marriott Fire Sprinkler Testing | 3 | 3 | 14-Aug-14 | 18-Aug-14 | 4 |
| **Fire Alarm** | | | | | | |
| CO-7116 | Fire Alarm Pre-Testing | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 2 |
| CO-7118 | City of Bellevue Fire Alarm Inspection / Approval | 3 | 3 | 13-Aug-14 | 15-Aug-14 | 2 |
| CO-7120 | Marriott Fire Alarm Testing | 3 | 3 | 18-Aug-14 | 20-Aug-14 | 2 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| CO-7100 | CO - Preliminary Start-Up & Testing | 20 | 20 | 09-Jul-14 | 05-Aug-14 | 0 |
| CO-7102 | CO - HVAC Commissioning | 40 | 40 | 06-Aug-14 | 01-Oct-14 | 0 |

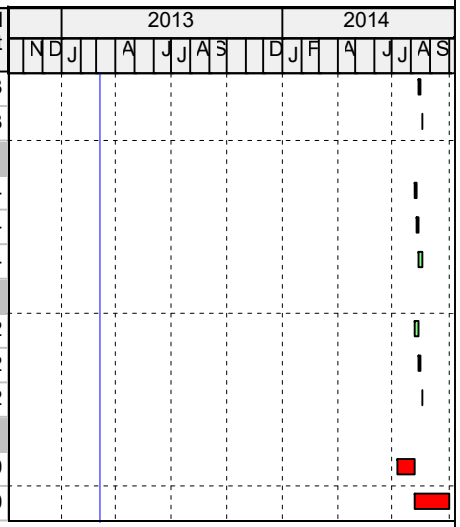



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Owner Baseline Schedule 10-7-13 Update** | | | | | | |
| MM-1000 | MM - Temporary Power Available | 86 | 0 | 08-Jul-13 A | 08-Jul-13 A | |
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13 A | | |
| CM-1002 | CM - Contract Time (578 Cal Days) | 576 | 365 | 06-Mar-13 A | 05-Oct-14 | 27 |
| CM-1014 | CM - Start of Construction | 0 | 0 | 05-Apr-13 A | | |
| CM-1006 | CM - Construction Documents Issued by Client - (w/i 1 | 0 | 0 | 06-Oct-13 | | 392 |
| CM-1008 | CM - Finalization of Allowances - (w/i 180 Days of NTF | 0 | 0 | 06-Oct-13 | | 392 |
| CO-7004 | CO - Prep / Submit O&M Manuals | 40 | 40 | 25-Jul-14 | 02-Sep-14 | 0 |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 24-Aug-14* | | 0 |
| CM-1016 | CM - Owner FF+E "Build-Out" | 42 | 42 | 24-Aug-14* | 04-Oct-14 | 0 |
| CM-1018 | CM - Hotel Operations Training | 21 | 21 | 14-Sep-14* | 04-Oct-14 | 0 |
| CO-7002 | CO - Final Inspections | 10 | 10 | 26-Sep-14 | 05-Oct-14 | 27 |
| CO-7006 | CO - Certificate of Occupancy | 0 | 0 | | 05-Oct-14 | 27 |
| CM-1026 | CM - Substantial Completion / Hotel Opening - (CCD) | 0 | 0 | | 01-Nov-14 | 0 |
| **Misc Milestones** | | | | | | |
| CM-1020 | MM - Site Mobilization | 10 | 0 | 06-Mar-13 A | 04-Apr-13 A | |
| MM-1004 | MM - Start Drywall In Tower | 0 | 0 | 14-Mar-14 | | 42 |
| MM-1008 | MM - Top Out - Tower / Structure | 0 | 0 | | 17-Apr-14 | 199 |
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 28-Jul-14 | 68 |
| MM-1010 | MM - Permanent Power Available | 0 | 0 | | 13-Aug-14 | 33 |
| **Executive Summary** | | | | | | |
| ES-1020 | Windows | 59 | 59 | 19-Feb-14 | 12-May-14 | 90 |
| ES-1016 | Metal Wall Panels @ Podium | 10 | 10 | 20-Mar-14 | 02-Apr-14 | 134 |

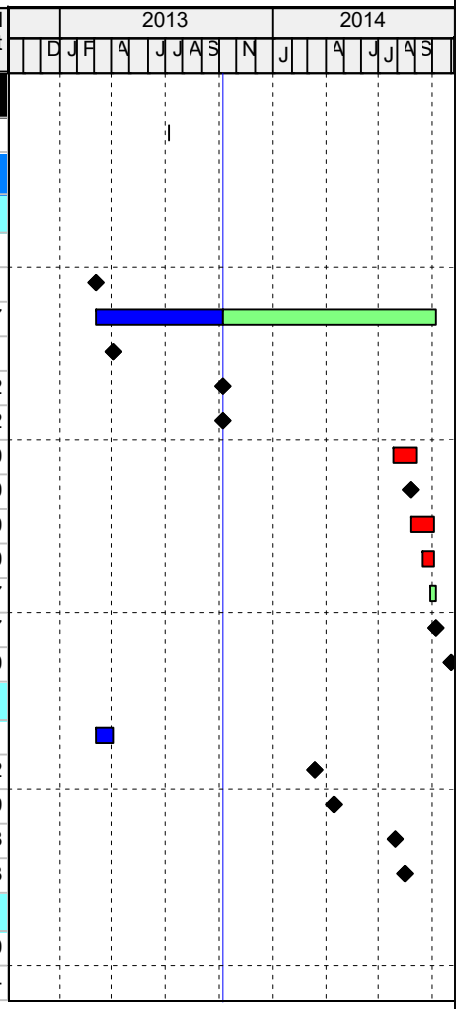


Actual Work | Remaining Work | Critical Remai... | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ES-1010 | Elevators | 97 | 97 | 15-May-14 | 01-Oct-14 | 22 |
| ES-1018 | Curtainwall East | 10 | 10 | 31-Jul-14 | 13-Aug-14 | 30 |
| ES-1022 | Start-Up / Testing / Commissioning | 40 | 40 | 04-Aug-14 | 29-Sep-14 | 1 |
| ES-1024 | Curtainwall South | 10 | 10 | 08-Sep-14 | 22-Sep-14 | 29 |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| Tower Crane | | | | | | |
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 0 | 04-Jun-13 A | 14-Jun-13 A | |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 0 | 20-Jun-13 A | 24-Jun-13 A | |
| TC-5902 | Tower Crane - Erectiion | 2 | 0 | 21-Jun-13 A | 24-Jun-13 A | |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 24-Jun-13 A | | |
| TC-5906 | Tower Crane - Operatational Period | 391 | 275 | 24-Jun-13 A | 07-Jul-14 | 115 |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 1 | 08-Jul-14 | 08-Jul-14 | 82 |
| Man & Material Lifts | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 5 | 10-Jan-14 | 16-Jan-14 | 197 |
| ML-5952 | Man/Material Lifts - Start Erectiion | 5 | 5 | 17-Jan-14 | 23-Jan-14 | 197 |
| ML-5954 | Man/Material Lifts - Load Test / Certify | 2 | 2 | 24-Jan-14 | 25-Jan-14 | 280 |
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 26-Jan-14 | | 280 |
| ML-5958 | Man/Material Lifts - Operatational Period | 216 | 216 | 26-Jan-14 | 29-Aug-14 | 44 |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 5 | 5 | 29-Aug-14 | 08-Sep-14 | 29 |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |
| Mass Excavation / Shoring | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 0 | 05-Apr-13 A | 12-Apr-13 A | |
| SW-2002 | Demolition And Utility Relocation | 8 | 0 | 15-Apr-13 A | 19-Apr-13 A | |
| Site Finishes | | | | | | |
| SW-2004 | Utility Connections | 30 | 30 | 02-Jul-14 | 13-Aug-14 | 16 |

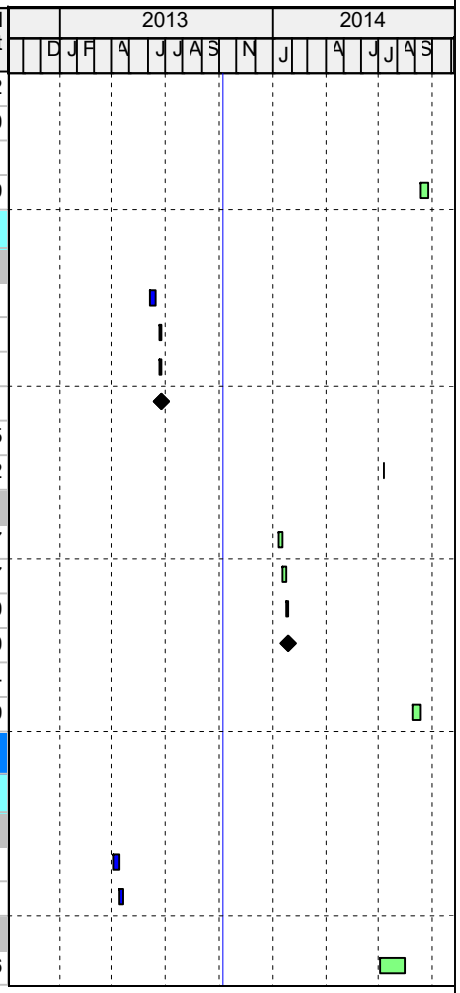



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2006 | Install Perm Power Electrical Service | 20 | 20 | 17-Jul-14 | 13-Aug-14 | 16 |
| SW-2008 | Sidewalks / Landscaping / Street Improvements | 40 | 40 | 14-Aug-14 | 09-Oct-14 | 16 |
| **Structure** | | | | | | |
| **Foundation / Substructure - (Levels LL4 / LL3)** | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 0 | 12-Jun-13 A | 27-Jun-13 A | |
| LL4-1601 | LL4 - Excavate Footings | 14 | 0 | 17-Jun-13 A | 30-Jul-13 A | |
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 0 | 18-Jun-13 A | 24-Jun-13 A | |
| LL4-1606 | LL4 - Undrgrnd Plumbing | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-1608 | LL4 - Undrgrnd Elec | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 0 | 19-Jun-13 A | 25-Jun-13 A | |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 0 | 26-Jun-13 A | 02-Aug-13 A | |
| LL4-2033 | LL4 - Shotcrete Walls | 27 | 0 | 26-Jun-13 A | 05-Aug-13 A | |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 0 | 03-Jul-13 A | 21-Aug-13 A | |
| LL4-1614 | LL4 - FRP SOG | 5 | 0 | 10-Jul-13 A | 07-Aug-13 A | |
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 0 | 12-Jul-13 A | 26-Jul-13 A | |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 0 | 13-Jul-13 A | 06-Aug-13 A | |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 0 | 22-Jul-13 A | 24-Jul-13 A | |
| LL4-1618 | LL4 - FRP Ramp SOG | 5 | 0 | 01-Aug-13 A | 07-Aug-13 A | |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2004 | LL2 - Shore / Form Deck | 8 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2006 | LL3 - M & E Inserts | 4 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2008 | LL3 - ReSteel / PT Cables | 6 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2010 | LL3 - Install Embeds | 2 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2001 | LL3 - Waterproof Walls | 3 | 0 | 05-Aug-13 A | 05-Aug-13 A | |
| LL3-2012 | LL3 - Pour / Finish Deck | 2 | 0 | 16-Aug-13 A | 16-Aug-13 A | |
| LL3-2014 | LL3 - Stress Tendons | 1 | 0 | 19-Aug-13 A | 19-Aug-13 A | |

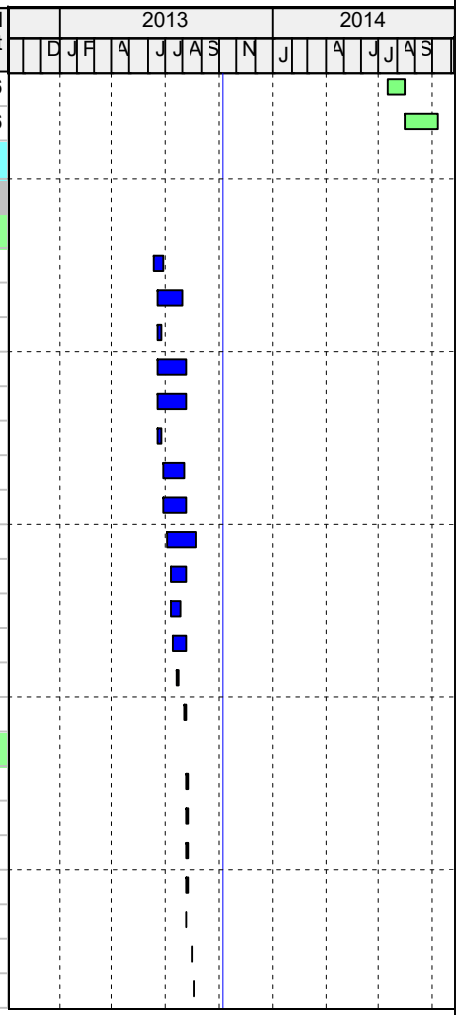



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-2000 | LL3 - FRP Core Walls | 8 | 0 | 19-Aug-13 A | 28-Aug-13 A | |
| LL3-2033 | LL3 - Shotcrete Walls | 5 | 0 | 23-Aug-13 A | 26-Aug-13 A | |
| LL3-2016 | LL3 - Strip / ReShore Deck | 3 | 0 | 01-Sep-13 A | 13-Sep-13 A | |
| LL3-2018 | LL3 - Remove ReShores | 4 | 4 | 05-Nov-13 | 08-Nov-13 | 111 |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Grids 1 to 4 - (SOG @ Loading Dock)** | | | | | | |
| LL2-2056 | LL2 - Grease Intercepter | 5 | 0 | 15-Aug-13 A | 21-Aug-13 A | |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 0 | 27-Aug-13 A | 04-Sep-13 A | |
| LL2-2027 | LL2 - Waterproof Walls | 2 | 0 | 27-Aug-13 A | 28-Aug-13 A | |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 0 | 30-Aug-13 A | 05-Sep-13 A | |
| LL2-2021 | LL2 - FRP Elec Vault | 14 | 0 | 30-Aug-13 A | 04-Sep-13 A | |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 0 | 04-Sep-13 A | 11-Sep-13 A | |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 0 | 11-Sep-13 A | 13-Sep-13 A | |
| LL2-2001 | LL2 - Excavation @ Loading Dock | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls/Roof | 11 | 0 | 19-Sep-13 A | 03-Oct-13 A | |
| LL2-2020 | LL2 - Undrgmd Plumbing | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2022 | LL2 - Undrgmd Elec | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2031 | LL2 - FRP Generator SOG | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2015 | LL2 to LL1 FRP Columns / Misc Walls | 6 | 3 | 01-Oct-13 A | 21-Oct-13 | 121 |
| LL2-2011 | LL2 - FRP Loading Dock Ftgs / Fndtns | 5 | 5 | 07-Oct-13 | 11-Oct-13 | 123 |
| LL2-2044 | LL2 - Set Generator | 1 | 1 | 07-Oct-13 | 07-Oct-13 | 270 |
| LL2-2029 | LL2 - Ftgs & Foundations @ LL2 SOG | 8 | 8 | 07-Oct-13 | 16-Oct-13 | 121 |
| LL2-2024 | LL2 - Cap Fill / Fine Grade | 4 | 4 | 14-Oct-13 | 17-Oct-13 | 123 |
| LL2-2017 | LL2 - FRP Loading Dock Lwr & Upr SOG's | 8 | 8 | 22-Oct-13 | 31-Oct-13 | 121 |
| LL2-2019 | LL2 - FRP Loading Dock Stairs | 4 | 4 | 01-Nov-13 | 06-Nov-13 | 121 |

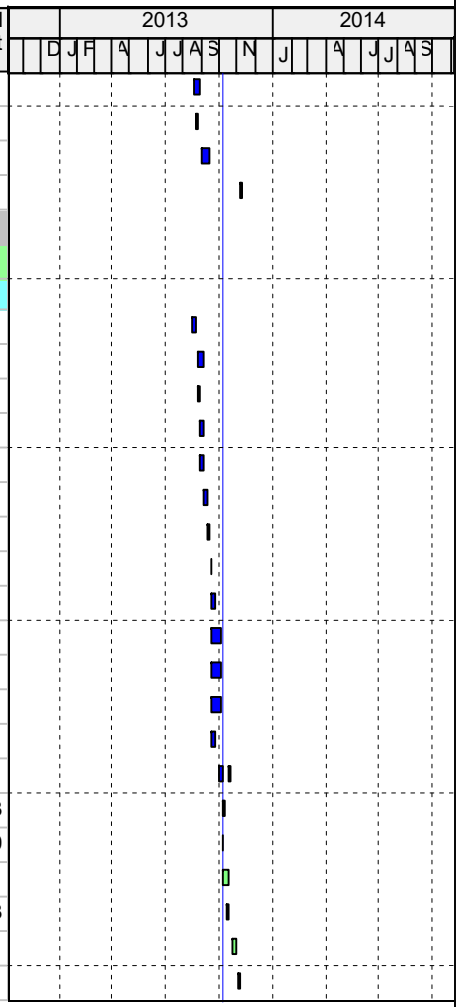



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |
| LL2-2004 | LL2 - Shore / Form Deck | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2035 | LL2 to LL1 - Shotcrete Walls | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2006 | LL2 - M & E Inserts | 4 | 0 | 14-Aug-13 A | 19-Aug-13 A | |
| LL2-2008 | LL2 - ReSteel / PT Cables | 6 | 0 | 14-Aug-13 A | 21-Aug-13 A | |
| LL2-2010 | LL2 - Install Embeds | 3 | 0 | 14-Aug-13 A | 16-Aug-13 A | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 0 | 27-Aug-13 A | 06-Sep-13 A | |
| LL2-2012 | LL2 - Place / Finish Deck | 3 | 0 | 29-Aug-13 A | 29-Aug-13 A | |
| LL2-2023 | LL2 - Waterproof Walls | 3 | 0 | 29-Aug-13 A | 03-Sep-13 A | |
| LL2-2014 | LL2 - Stress Tendons | 1 | 0 | 30-Aug-13 A | 30-Aug-13 A | |
| LL2-2016 | LL2 - Strip / ReShore | 3 | 0 | 03-Sep-13 A | 05-Sep-13 A | |
| LL2-8234 | LL2 - Place / Finish Deck | 3 | 0 | 12-Sep-13 A | 12-Sep-13 A | |
| LL2-2000 | LL2 - FRP Core Walls | 8 | 0 | 12-Sep-13 A | 23-Sep-13 A | |
| LL2-2013 | LL2 - Pour / Finish Ramp | 1 | 1 | 07-Oct-13 | 07-Oct-13 | 41 |
| LL2-2018 | LL2 - Remove ReShores | 4 | 4 | 26-Nov-13 | 03-Dec-13 | 7 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| P5A-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2000 | LL1 - FRP Core Walls | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2004 | LL1 - Shore / Form Deck | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| P6-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P6-2004 | LL1 - Shore / Form Deck | 7 | 0 | 16-Sep-13 A | 24-Sep-13 A | |
| P5A-2006 | LL1 - MEP Rough In | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2008 | LL1 - ReSteel / PT Cables | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2012 | LL1 - Place / Finish Deck | 0 | 0 | 20-Sep-13 A | | |
| P5A-2020 | LL1 - Waterproof Walls | 3 | 0 | 20-Sep-13 A | 24-Sep-13 A | |
| P5A-2014 | LL1 - Stress Tendons | 1 | 0 | 23-Sep-13 A | 23-Sep-13 A | |

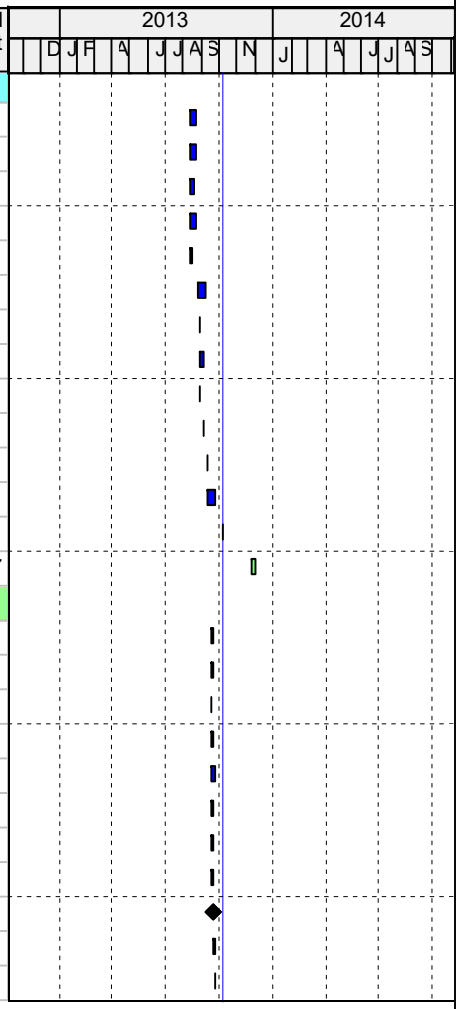



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P5A-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2006 | LL1 - MEP Rough In | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2008 | LL1 - ReSteel / PT Cables | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 24-Sep-13 A | 25-Sep-13 A | |
| P6-2020 | LL1 - Waterproof Walls | 4 | 0 | 24-Sep-13 A | 27-Sep-13 A | |
| P5A-2033 | LL1 - Resteel/Shotcrete Walls | 3 | 0 | 25-Sep-13 A | 27-Sep-13 A | |
| P5B-2002 | LL1 - FRP Columns Below | 5 | 0 | 26-Sep-13 A | 02-Oct-13 A | |
| P5B-2004 | LL1 - Shore / Form Deck | 7 | 0 | 26-Sep-13 A | 04-Oct-13 A | |
| P6-2012 | LL1 - Place / Finish Deck | 0 | 0 | 27-Sep-13 A | | |
| P6-2014 | LL1 - Stress Tendons | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2033 | LL1 - Resteel/Shotcrete Walls | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 01-Oct-13 A | 03-Oct-13 A | |
| P5B-2006 | LL1 - MEP Rough In | 5 | 3 | 03-Oct-13 A | 09-Oct-13 | -24 |
| P10A--2002 | FRP Columns Below | 5 | 3 | 03-Oct-13 A | 09-Oct-13 | 269 |
| P10A--2004 | Shore / Form Deck | 4 | 2 | 03-Oct-13 A | 08-Oct-13 | 23 |
| P5B-2008 | LL1 - ReSteel / PT Cables | 5 | 4 | 04-Oct-13 A | 10-Oct-13 | -25 |
| P5B-2010 | LL1 - Install Edgeform/Embeds | 4 | 3 | 04-Oct-13 A | 09-Oct-13 | -24 |
| P8-2002 | FRP Columns Below | 5 | 5 | 07-Oct-13 | 11-Oct-13 | 267 |
| P8-2000 | Form/Resteel/Close Core Walls | 14 | 14 | 07-Oct-13 | 24-Oct-13 | 23 |
| P8-2004 | Shore / Form Deck P8 | 8 | 8 | 07-Oct-13 | 16-Oct-13 | 23 |
| P7-2002 | FRP Columns Below | 5 | 5 | 08-Oct-13 | 14-Oct-13 | 266 |
| P7-2004 | Shore / Form Deck | 6 | 6 | 08-Oct-13 | 15-Oct-13 | 256 |
| P10A--2006 | MEP Rough In | 3 | 3 | 08-Oct-13 | 10-Oct-13 | 35 |
| P10A--2008 | ReSteel / PT Cables | 3 | 3 | 08-Oct-13 | 10-Oct-13 | 35 |
| P10A--2010 | Install Edgeform/Embeds | 2 | 2 | 08-Oct-13 | 09-Oct-13 | 36 |
| P5B-2012 | LL1 - Place / Finish Deck | 0 | 0 | 11-Oct-13 | | -25 |
| P10A--2012 | Place / Finish Deck | 0 | 0 | 11-Oct-13 | | 35 |

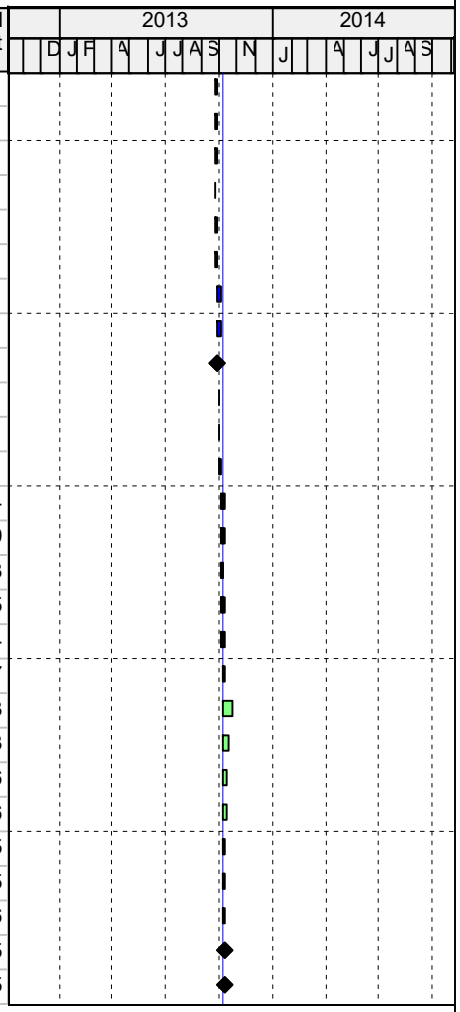



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P5B-2014 | LL1 - Stress Tendons | 1 | 1 | 14-Oct-13 | 14-Oct-13 | 259 |
| P7-2006 | MEP Rough In | 4 | 4 | 14-Oct-13 | 17-Oct-13 | 256 |
| P7-2008 | ReSteel / PT Cables | 4 | 4 | 14-Oct-13 | 17-Oct-13 | 256 |
| P10A--2014 | Stress Tendons | 1 | 1 | 14-Oct-13 | 14-Oct-13 | 35 |
| P8-2020 | Shore / Form Deck P9 | 6 | 6 | 14-Oct-13 | 21-Oct-13 | -25 |
| P5B-2016 | LL1 - Strip / ReShore Deck | 3 | 3 | 15-Oct-13 | 17-Oct-13 | 259 |
| P7-2010 | Install Edgeform/Embeds | 2 | 2 | 15-Oct-13 | 16-Oct-13 | 257 |
| P8-2006 | MEP Rough In | 8 | 8 | 15-Oct-13 | 24-Oct-13 | 23 |
| P8-2008 | ReSteel / PT Cables | 8 | 8 | 15-Oct-13 | 24-Oct-13 | 23 |
| P8-2010 | Install Edgeform/Embeds | 4 | 4 | 15-Oct-13 | 18-Oct-13 | 27 |
| P10A--2016 | Strip / ReShore Deck | 3 | 3 | 15-Oct-13 | 17-Oct-13 | 35 |
| P7-2012 | Place / Finish Deck | 0 | 0 | 18-Oct-13 | | 256 |
| P7-2033 | Resteel/Shotcrete Walls | 3 | 3 | 18-Oct-13 | 22-Oct-13 | 260 |
| P7-2014 | Stress Tendons | 1 | 1 | 21-Oct-13 | 21-Oct-13 | 256 |
| P7-2016 | Strip / ReShore Deck | 3 | 3 | 22-Oct-13 | 24-Oct-13 | 256 |
| P10B--2002 | FRP Columns Below | 5 | 5 | 22-Oct-13 | 28-Oct-13 | 256 |
| P10B--2000 | FRP Shear Walls Below | 3 | 3 | 22-Oct-13 | 24-Oct-13 | 258 |
| P10B--2004 | Shore / Form Deck | 6 | 6 | 22-Oct-13 | 29-Oct-13 | -25 |
| P8-2012 | Place / Finish Deck P 8 & 9 and Core Walls | 0 | 0 | 25-Oct-13 | | 23 |
| P8-2014 | Stress Tendons | 1 | 1 | 28-Oct-13 | 28-Oct-13 | 23 |
| P8-2016 | Strip / ReShore Deck | 3 | 3 | 29-Oct-13 | 31-Oct-13 | 23 |
| P10B--2006 | MEP Rough In | 3 | 3 | 29-Oct-13 | 31-Oct-13 | 22 |
| P10B--2008 | ReSteel / PT Cables | 3 | 3 | 29-Oct-13 | 31-Oct-13 | 22 |
| P10B--2010 | Install Edgeform/Embeds | 3 | 3 | 29-Oct-13 | 31-Oct-13 | 22 |
| P11--2002 | FRP Columns Below | 5 | 5 | 30-Oct-13 | 05-Nov-13 | 250 |
| P11--2004 | Shore / Form Deck | 5 | 5 | 30-Oct-13 | 05-Nov-13 | -25 |
| P10B--2012 | Place / Finish Deck | 0 | 0 | 01-Nov-13 | | 22 |

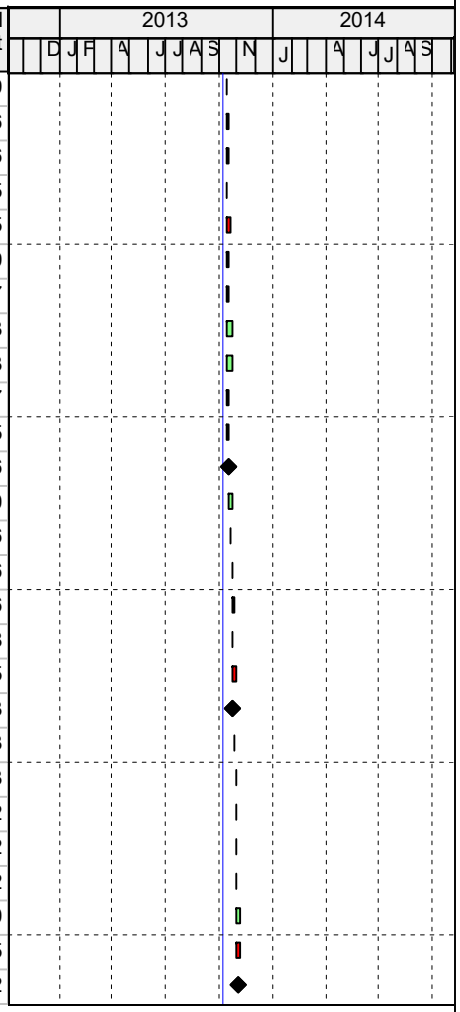



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P10B–2014 | Stress Tendons | 1 | 1 | 04-Nov-13 | 04-Nov-13 | 22 |
| P10B–2016 | Strip / ReShore Deck | 3 | 3 | 05-Nov-13 | 07-Nov-13 | 22 |
| P11–2006 | MEP Rough In | 3 | 3 | 05-Nov-13 | 07-Nov-13 | 241 |
| P11–2008 | ReSteel / PT Cables | 3 | 3 | 05-Nov-13 | 07-Nov-13 | 241 |
| P11–2010 | Install Edgeform/Embeds | 3 | 3 | 05-Nov-13 | 07-Nov-13 | 241 |
| P12–2002 | FRP Columns Below | 5 | 5 | 06-Nov-13 | 13-Nov-13 | 245 |
| P12–2000 | Form/Resteel/Close Core Walls | 10 | 10 | 06-Nov-13 | 20-Nov-13 | 8 |
| P12–2004 | Shore / Form Deck | 7 | 7 | 06-Nov-13 | 15-Nov-13 | -25 |
| P11–2012 | Place / Finish Deck | 0 | 0 | 08-Nov-13 | | 241 |
| P11–2014 | Stress Tendons | 1 | 1 | 12-Nov-13 | 12-Nov-13 | 241 |
| P11–2016 | Strip / ReShore Deck | 3 | 3 | 13-Nov-13 | 15-Nov-13 | 241 |
| P12–2006 | MEP Rough In | 5 | 5 | 15-Nov-13 | 21-Nov-13 | 7 |
| P12–2008 | ReSteel / PT Cables | 5 | 5 | 15-Nov-13 | 21-Nov-13 | 7 |
| P12–2010 | Install Edgeform/Embeds | 5 | 5 | 15-Nov-13 | 21-Nov-13 | 7 |
| P13–2002 | FRP Columns Below | 5 | 5 | 18-Nov-13 | 22-Nov-13 | 238 |
| P13–2004 | Shore / Form Deck | 9 | 9 | 18-Nov-13 | 02-Dec-13 | -25 |
| P13A–2002 | FRP Columns Below | 5 | 5 | 18-Nov-13 | 22-Nov-13 | 238 |
| P13A–2004 | Shore / Form Deck | 9 | 9 | 18-Nov-13 | 02-Dec-13 | 224 |
| P12–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 22-Nov-13 | | 7 |
| P12–2014 | Stress Tendons | 1 | 1 | 25-Nov-13 | 25-Nov-13 | 7 |
| P12–2016 | Strip / ReShore Deck | 3 | 3 | 26-Nov-13 | 02-Dec-13 | 13 |
| P13–2006 | MEP Rough In | 5 | 5 | 27-Nov-13 | 05-Dec-13 | 222 |
| P13–2008 | ReSteel / PT Cables | 5 | 5 | 27-Nov-13 | 05-Dec-13 | 222 |
| P13–2010 | Install Edgeform/Embeds | 5 | 5 | 27-Nov-13 | 05-Dec-13 | 222 |
| P13A–2006 | MEP Rough In | 4 | 4 | 02-Dec-13 | 05-Dec-13 | 224 |
| P13A–2008 | ReSteel / PT Cables | 4 | 4 | 02-Dec-13 | 05-Dec-13 | 224 |
| P13A–2010 | Install Edgeform/Embeds | 4 | 4 | 02-Dec-13 | 05-Dec-13 | 224 |

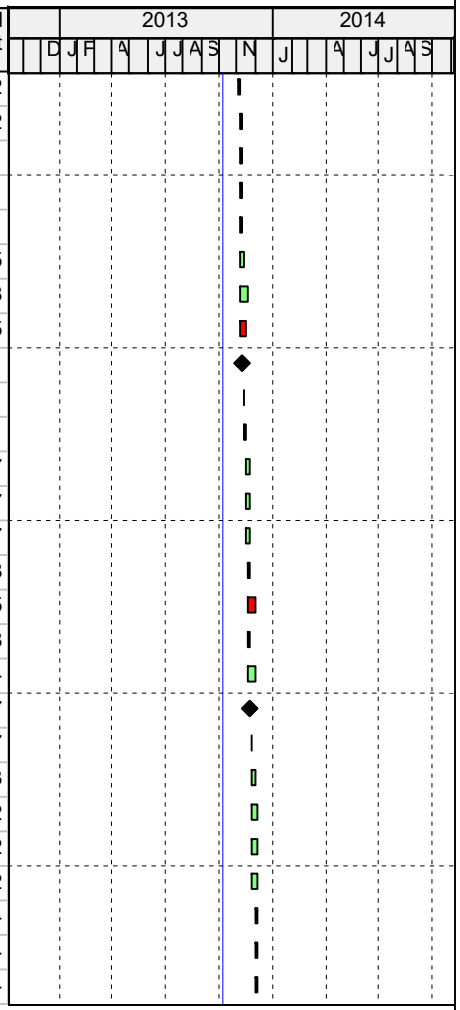



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P14–2002 | FRP Columns Below | 5 | 5 | 03-Dec-13 | 09-Dec-13 | 229 |
| P14–2000 | Form/Resteel/Close Core Walls | 13 | 13 | 03-Dec-13 | 19-Dec-13 | 221 |
| P14–2004 | Shore / Form Deck | 9 | 9 | 03-Dec-13 | 13-Dec-13 | -25 |
| P13–2012 | Place / Finish Deck | 0 | 0 | 06-Dec-13 | | 222 |
| P13A–2012 | Place / Finish Deck | 0 | 0 | 06-Dec-13 | | 224 |
| P13–2014 | Stress Tendons | 1 | 1 | 09-Dec-13 | 09-Dec-13 | 222 |
| P13A–2014 | Stress Tendons | 1 | 1 | 09-Dec-13 | 09-Dec-13 | 224 |
| P13–2016 | Strip / ReShore Deck | 3 | 3 | 10-Dec-13 | 12-Dec-13 | 222 |
| P13A–2016 | Strip / ReShore Deck | 3 | 3 | 10-Dec-13 | 12-Dec-13 | 224 |
| P14–2006 | MEP Rough In | 5 | 5 | 13-Dec-13 | 19-Dec-13 | -25 |
| P14–2008 | ReSteel / PT Cables | 5 | 5 | 13-Dec-13 | 19-Dec-13 | -25 |
| P14–2010 | Install Edgeform/Embeds | 5 | 5 | 13-Dec-13 | 19-Dec-13 | -25 |
| P14–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 20-Dec-13 | | -25 |
| P14–2014 | Stress Tendons | 1 | 1 | 23-Dec-13 | 23-Dec-13 | -25 |
| P15–2002 | FRP Columns Below | 7 | 7 | 23-Dec-13 | 02-Jan-14 | 213 |
| P15–2000 | Jump/Resteel/Close Core | 7 | 7 | 23-Dec-13 | 02-Jan-14 | 213 |
| P15–2004 | Shore / Form Deck | 5 | 5 | 23-Dec-13 | 30-Dec-13 | -25 |
| P5A-2018 | LL1 - Remove Reshores | 2 | 2 | 24-Dec-13 | 26-Dec-13 | 68 |
| P14–2016 | Strip / ReShore Deck | 3 | 3 | 24-Dec-13 | 27-Dec-13 | 18 |
| P6-2018 | LL1 - Remove Reshores | 2 | 2 | 27-Dec-13 | 30-Dec-13 | 68 |
| P15–2006 | MEP Rough In | 3 | 3 | 30-Dec-13 | 02-Jan-14 | -25 |
| P15–2008 | ReSteel / PT Cables | 3 | 3 | 30-Dec-13 | 02-Jan-14 | -25 |
| P15–2010 | Install Edgeform/Embeds | 2 | 2 | 30-Dec-13 | 31-Dec-13 | -24 |
| P5B-2018 | LL1 - Remove Reshores | 2 | 2 | 31-Dec-13 | 02-Jan-14 | 211 |
| P7-2018 | Remove Reshores | 2 | 2 | 03-Jan-14 | 06-Jan-14 | 211 |
| P15–2012 | Place / Finish Deck | 0 | 0 | 03-Jan-14 | | -25 |
| P15–2020 | Place Conc @ Core | 0 | 0 | 03-Jan-14 | | 213 |

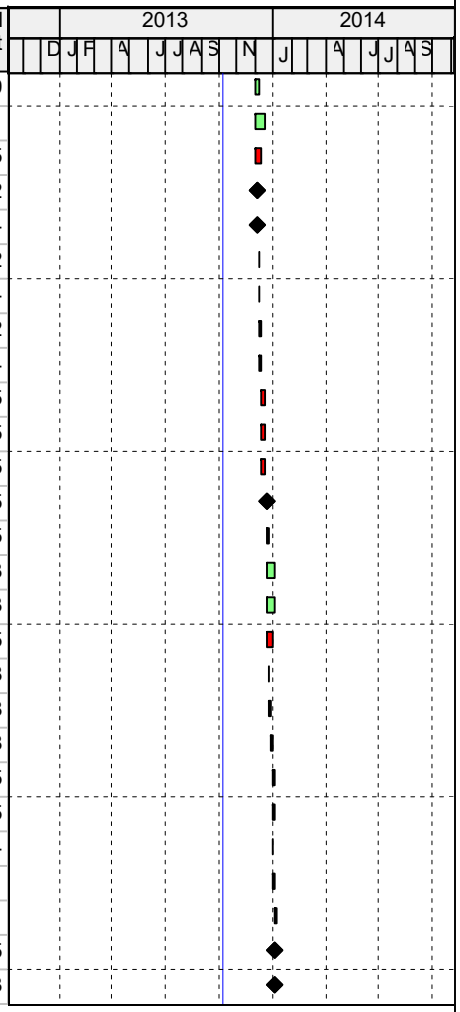


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P15–2014 | Stress Tendons | 1 | 1 | 06-Jan-14 | 06-Jan-14 | -19 |
| P16-2002 | FRP Columns Below | 5 | 5 | 06-Jan-14 | 10-Jan-14 | 207 |
| P16-2000 | Jump/Resteel/Close Core | 4 | 4 | 06-Jan-14 | 09-Jan-14 | 208 |
| P16-2004 | Shore / Form Deck | 3 | 3 | 06-Jan-14 | 08-Jan-14 | -25 |
| P8-2018 | Remove Reshores | 2 | 2 | 07-Jan-14 | 08-Jan-14 | -19 |
| P15–2016 | Strip / ReShore Deck | 3 | 3 | 07-Jan-14 | 09-Jan-14 | 47 |
| P16-2006 | MEP Rough In | 2 | 2 | 08-Jan-14 | 09-Jan-14 | -25 |
| P16-2008 | ReSteel / PT Cables | 2 | 2 | 08-Jan-14 | 09-Jan-14 | -25 |
| P16-2010 | Install Edgeform/Embeds | 2 | 2 | 08-Jan-14 | 09-Jan-14 | -25 |
| P10A–2018 | Remove Reshores | 2 | 2 | 09-Jan-14 | 10-Jan-14 | -19 |
| P16-2012 | Place / Finish Deck | 0 | 0 | 10-Jan-14 | | -25 |
| P16-2020 | Place Conc @ Core | 0 | 0 | 10-Jan-14 | | 208 |
| P10B–2018 | Remove Reshores | 2 | 2 | 13-Jan-14 | 14-Jan-14 | -19 |
| P16-2014 | Stress Tendons | 1 | 1 | 13-Jan-14 | 13-Jan-14 | -25 |
| P17-2002 | FRP Columns Below | 5 | 5 | 13-Jan-14 | 17-Jan-14 | 202 |
| P17-2000 | Jump/Resteel/Close Core | 4 | 4 | 13-Jan-14 | 16-Jan-14 | 203 |
| P17-2004 | Shore / Form Deck | 3 | 3 | 13-Jan-14 | 15-Jan-14 | -15 |
| P12–2018 | Remove Reshores | 2 | 2 | 14-Jan-14 | 15-Jan-14 | -15 |
| P16-2016 | Strip / ReShore Deck | 3 | 3 | 14-Jan-14 | 16-Jan-14 | 47 |
| P11–2018 | Remove Reshores | 2 | 2 | 15-Jan-14 | 16-Jan-14 | 203 |
| P17-2006 | MEP Rough In | 2 | 2 | 15-Jan-14 | 16-Jan-14 | -15 |
| P17-2008 | ReSteel / PT Cables | 2 | 2 | 15-Jan-14 | 16-Jan-14 | -15 |
| P17-2010 | Install Edgeform/Embeds | 2 | 2 | 15-Jan-14 | 16-Jan-14 | -15 |
| P17-2012 | Place / Finish Deck | 0 | 0 | 17-Jan-14 | | -15 |
| P17-2020 | Place Conc @ Core | 0 | 0 | 17-Jan-14 | | 203 |
| P17-2014 | Stress Tendons | 1 | 1 | 20-Jan-14 | 20-Jan-14 | 47 |
| P18-2002 | FRP Columns Below | 5 | 5 | 20-Jan-14 | 24-Jan-14 | 197 |

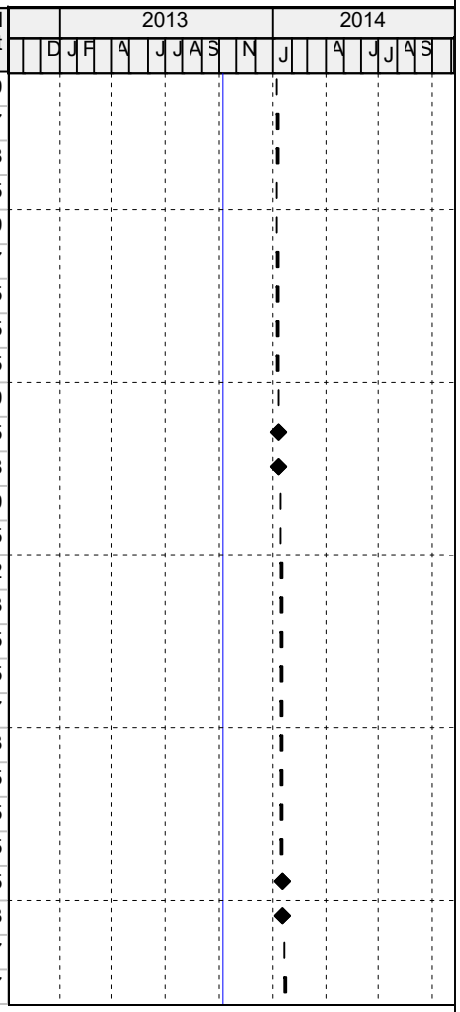



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P18-2000 | Jump/Resteel/Close Core | 4 | 4 | 20-Jan-14 | 23-Jan-14 | 198 |
| P18-2004 | Shore / Form Deck | 3 | 3 | 20-Jan-14 | 22-Jan-14 | -15 |
| P13--2018 | Remove Reshores | 2 | 2 | 21-Jan-14 | 22-Jan-14 | 197 |
| P17-2016 | Strip / ReShore Deck | 3 | 3 | 21-Jan-14 | 23-Jan-14 | 47 |
| P18-2006 | MEP Rough In | 2 | 2 | 22-Jan-14 | 23-Jan-14 | -15 |
| P18-2008 | ReSteel / PT Cables | 2 | 2 | 22-Jan-14 | 23-Jan-14 | -15 |
| P18-2010 | Install Edgeform/Embeds | 2 | 2 | 22-Jan-14 | 23-Jan-14 | -15 |
| P13A--2018 | Remove Reshores | 2 | 2 | 23-Jan-14 | 24-Jan-14 | 197 |
| P18-2012 | Place / Finish Deck | 0 | 0 | 24-Jan-14 | | -15 |
| P18-2020 | Place Conc @ Core | 0 | 0 | 24-Jan-14 | | 198 |
| P18-2014 | Stress Tendons | 1 | 1 | 27-Jan-14 | 27-Jan-14 | -2 |
| P19-2002 | FRP Columns Below | 5 | 5 | 27-Jan-14 | 31-Jan-14 | 192 |
| P19-2000 | Jump/Resteel/Close Core | 4 | 4 | 27-Jan-14 | 30-Jan-14 | 193 |
| P19-2004 | Shore / Form Deck | 3 | 3 | 27-Jan-14 | 29-Jan-14 | -15 |
| P14--2018 | Remove Reshores | 2 | 2 | 28-Jan-14 | 29-Jan-14 | -2 |
| P18-2016 | Strip / ReShore Deck | 3 | 3 | 28-Jan-14 | 30-Jan-14 | 47 |
| P19-2006 | MEP Rough In | 2 | 2 | 29-Jan-14 | 30-Jan-14 | -15 |
| P19-2008 | ReSteel / PT Cables | 2 | 2 | 29-Jan-14 | 30-Jan-14 | -15 |
| P19-2010 | Install Edgeform/Embeds | 2 | 2 | 29-Jan-14 | 30-Jan-14 | -15 |
| P19-2012 | Place / Finish Deck | 0 | 0 | 31-Jan-14 | | -15 |
| P19-2020 | Place Conc @ Core | 0 | 0 | 31-Jan-14 | | 193 |
| P19-2014 | Stress Tendons | 1 | 1 | 03-Feb-14 | 03-Feb-14 | 30 |
| P20-2002 | FRP Columns Below | 5 | 5 | 03-Feb-14 | 07-Feb-14 | 187 |
| P20-2000 | Jump/Resteel/Close Core | 4 | 4 | 03-Feb-14 | 06-Feb-14 | 188 |
| P20-2004 | Shore / Form Deck | 3 | 3 | 03-Feb-14 | 05-Feb-14 | -15 |
| P15--2018 | Remove Reshores | 2 | 2 | 04-Feb-14 | 05-Feb-14 | 30 |
| P19-2016 | Strip / ReShore Deck | 3 | 3 | 04-Feb-14 | 06-Feb-14 | 47 |

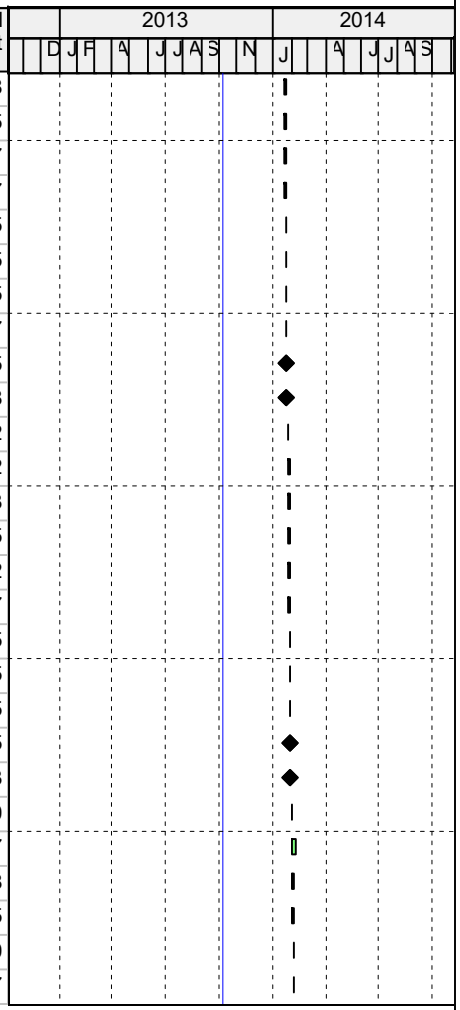



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P20-2006 | MEP Rough In | 2 | 2 | 05-Feb-14 | 06-Feb-14 | -15 |
| P20-2008 | ReSteel / PT Cables | 2 | 2 | 05-Feb-14 | 06-Feb-14 | -15 |
| P20-2010 | Install Edgeform/Embeds | 2 | 2 | 05-Feb-14 | 06-Feb-14 | -15 |
| P20-2012 | Place / Finish Deck | 0 | 0 | 07-Feb-14 | | -15 |
| P20-2020 | Place Conc @ Core | 0 | 0 | 07-Feb-14 | | 188 |
| P20-2014 | Stress Tendons | 1 | 1 | 10-Feb-14 | 10-Feb-14 | 30 |
| P21-2002 | FRP Columns Below | 5 | 5 | 10-Feb-14 | 14-Feb-14 | 182 |
| P21-2000 | Jump/Resteel/Close Core | 4 | 4 | 10-Feb-14 | 13-Feb-14 | 183 |
| P21-2004 | Shore / Form Deck | 3 | 3 | 10-Feb-14 | 12-Feb-14 | -15 |
| P16-2018 | Remove Reshores | 2 | 2 | 11-Feb-14 | 12-Feb-14 | 30 |
| P20-2016 | Strip / ReShore Deck | 3 | 3 | 11-Feb-14 | 13-Feb-14 | 47 |
| P21-2006 | MEP Rough In | 2 | 2 | 12-Feb-14 | 13-Feb-14 | -15 |
| P21-2008 | ReSteel / PT Cables | 2 | 2 | 12-Feb-14 | 13-Feb-14 | -15 |
| P21-2010 | Install Edgeform/Embeds | 2 | 2 | 12-Feb-14 | 13-Feb-14 | -15 |
| P21-2012 | Place / Finish Deck | 0 | 0 | 14-Feb-14 | | -15 |
| P21-2020 | Place Conc @ Core | 0 | 0 | 14-Feb-14 | | 183 |
| P21-2014 | Stress Tendons | 1 | 1 | 17-Feb-14 | 17-Feb-14 | 30 |
| P22-2002 | FRP Columns Below | 5 | 5 | 17-Feb-14 | 21-Feb-14 | 177 |
| P22-2000 | Jump/Resteel/Close Core | 4 | 4 | 17-Feb-14 | 20-Feb-14 | 178 |
| P22-2004 | Shore / Form Deck | 3 | 3 | 17-Feb-14 | 19-Feb-14 | -15 |
| P17-2018 | Remove Reshores | 2 | 2 | 18-Feb-14 | 19-Feb-14 | 30 |
| P21-2016 | Strip / ReShore Deck | 3 | 3 | 18-Feb-14 | 20-Feb-14 | 47 |
| P22-2006 | MEP Rough In | 2 | 2 | 19-Feb-14 | 20-Feb-14 | -15 |
| P22-2008 | ReSteel / PT Cables | 2 | 2 | 19-Feb-14 | 20-Feb-14 | -15 |
| P22-2010 | Install Edgeform/Embeds | 2 | 2 | 19-Feb-14 | 20-Feb-14 | -15 |
| P22-2012 | Place / Finish Deck | 0 | 0 | 21-Feb-14 | | -15 |
| P22-2020 | Place Conc @ Core | 0 | 0 | 21-Feb-14 | | 178 |

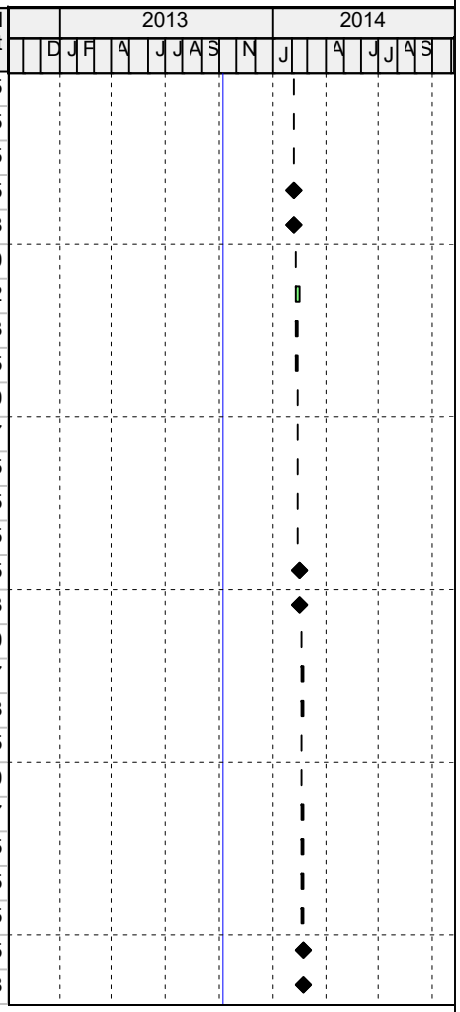



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P22-2014 | Stress Tendons | 1 | 1 | 24-Feb-14 | 24-Feb-14 | 30 |
| P23-2002 | FRP Columns Below | 5 | 5 | 24-Feb-14 | 28-Feb-14 | 172 |
| P23-2000 | Jump/Resteel/Close Core | 4 | 4 | 24-Feb-14 | 27-Feb-14 | 173 |
| P23-2004 | Shore / Form Deck | 3 | 3 | 24-Feb-14 | 26-Feb-14 | -15 |
| P18-2018 | Remove Reshores | 2 | 2 | 25-Feb-14 | 26-Feb-14 | 30 |
| P22-2016 | Strip / ReShore Deck | 3 | 3 | 25-Feb-14 | 27-Feb-14 | 47 |
| P23-2006 | MEP Rough In | 2 | 2 | 26-Feb-14 | 27-Feb-14 | -15 |
| P23-2008 | ReSteel / PT Cables | 2 | 2 | 26-Feb-14 | 27-Feb-14 | -15 |
| P23-2010 | Install Edgeform/Embeds | 2 | 2 | 26-Feb-14 | 27-Feb-14 | -15 |
| P23-2012 | Place / Finish Deck | 0 | 0 | 28-Feb-14 | | -15 |
| P23-2020 | Place Conc @ Core | 0 | 0 | 28-Feb-14 | | 173 |
| P23-2014 | Stress Tendons | 1 | 1 | 03-Mar-14 | 03-Mar-14 | 30 |
| P24-2002 | FRP Columns Below | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 167 |
| P24-2000 | Jump/Resteel/Close Core | 4 | 4 | 03-Mar-14 | 06-Mar-14 | 168 |
| P24-2004 | Shore / Form Deck | 3 | 3 | 03-Mar-14 | 05-Mar-14 | -15 |
| P19-2018 | Remove Reshores | 2 | 2 | 04-Mar-14 | 05-Mar-14 | 30 |
| P23-2016 | Strip / ReShore Deck | 3 | 3 | 04-Mar-14 | 06-Mar-14 | 66 |
| P24-2006 | MEP Rough In | 2 | 2 | 05-Mar-14 | 06-Mar-14 | -15 |
| P24-2008 | ReSteel / PT Cables | 2 | 2 | 05-Mar-14 | 06-Mar-14 | -15 |
| P24-2010 | Install Edgeform/Embeds | 2 | 2 | 05-Mar-14 | 06-Mar-14 | -15 |
| P24-2012 | Place / Finish Deck | 0 | 0 | 07-Mar-14 | | -15 |
| P24-2020 | Place Conc @ Core | 0 | 0 | 07-Mar-14 | | 168 |
| P24-2014 | Stress Tendons | 1 | 1 | 10-Mar-14 | 10-Mar-14 | 30 |
| P25-2002 | FRP Columns Below | 5 | 5 | 10-Mar-14 | 14-Mar-14 | 162 |
| P25-2000 | Jump/Resteel/Close Core | 4 | 4 | 10-Mar-14 | 13-Mar-14 | 163 |
| P25-2004 | Shore / Form Deck | 3 | 3 | 10-Mar-14 | 12-Mar-14 | -15 |
| P20-2018 | Remove Reshores | 2 | 2 | 11-Mar-14 | 12-Mar-14 | 30 |

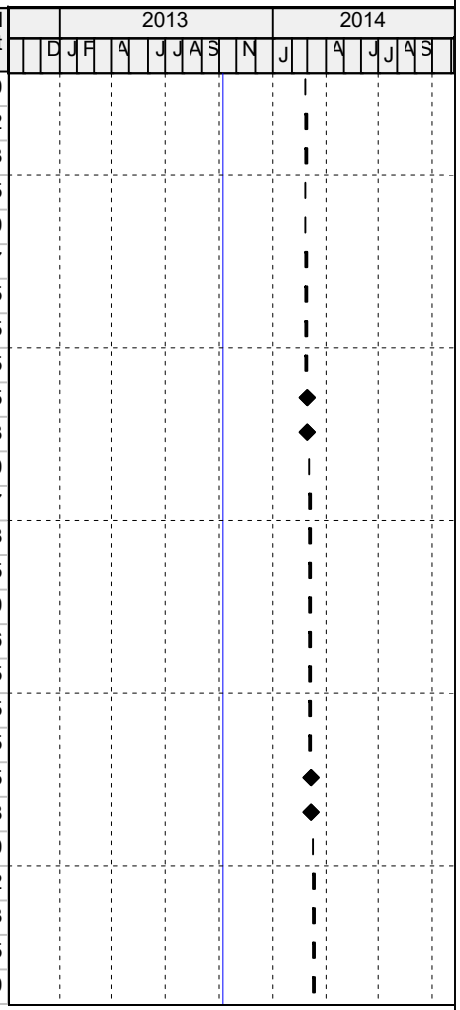



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P24-2016 | Strip / ReShore Deck | 3 | 3 | 11-Mar-14 | 13-Mar-14 | 66 |
| P25-2006 | MEP Rough In | 2 | 2 | 12-Mar-14 | 13-Mar-14 | -15 |
| P25-2008 | ReSteel / PT Cables | 2 | 2 | 12-Mar-14 | 13-Mar-14 | -15 |
| P25-2010 | Install Edgeform/Embeds | 2 | 2 | 12-Mar-14 | 13-Mar-14 | -15 |
| P25-2012 | Place / Finish Deck | 0 | 0 | 14-Mar-14 | | -15 |
| P25-2020 | Place Conc @ Core | 0 | 0 | 14-Mar-14 | | 163 |
| P26-2002 | FRP Columns Below | 5 | 5 | 17-Mar-14 | 21-Mar-14 | 157 |
| P26-2000 | Jump/Resteel/Close Core | 4 | 4 | 17-Mar-14 | 20-Mar-14 | 158 |
| P26-2004 | Shore / Form Deck | 3 | 3 | 17-Mar-14 | 19-Mar-14 | -15 |
| P25-2014 | Stress Tendons | 1 | 1 | 17-Mar-14 | 17-Mar-14 | 4 |
| P21-2018 | Remove Reshores | 2 | 2 | 18-Mar-14 | 19-Mar-14 | 30 |
| P25-2016 | Strip / ReShore Deck | 3 | 3 | 18-Mar-14 | 20-Mar-14 | 4 |
| P26-2006 | MEP Rough In | 2 | 2 | 19-Mar-14 | 20-Mar-14 | -15 |
| P26-2008 | ReSteel / PT Cables | 2 | 2 | 19-Mar-14 | 20-Mar-14 | -15 |
| P26-2010 | Install Edgeform/Embeds | 2 | 2 | 19-Mar-14 | 20-Mar-14 | -15 |
| P26-2012 | Place / Finish Deck | 0 | 0 | 21-Mar-14 | | -15 |
| P26-2020 | Place Conc @ Core | 0 | 0 | 21-Mar-14 | | 158 |
| P27-2002 | FRP Columns Below | 5 | 5 | 24-Mar-14 | 28-Mar-14 | 152 |
| P27-2000 | Jump/Resteel/Close Core | 4 | 4 | 24-Mar-14 | 27-Mar-14 | 153 |
| P27-2004 | Shore / Form Deck | 3 | 3 | 24-Mar-14 | 26-Mar-14 | -15 |
| P26-2014 | Stress Tendons | 1 | 1 | 24-Mar-14 | 24-Mar-14 | 1 |
| P22-2018 | Remove Reshores | 2 | 2 | 25-Mar-14 | 26-Mar-14 | 30 |
| P26-2016 | Strip / ReShore Deck | 3 | 3 | 25-Mar-14 | 27-Mar-14 | 1 |
| P27-2006 | MEP Rough In | 2 | 2 | 26-Mar-14 | 27-Mar-14 | -15 |
| P27-2008 | ReSteel / PT Cables | 2 | 2 | 26-Mar-14 | 27-Mar-14 | -15 |
| P27-2010 | Install Edgeform/Embeds | 2 | 2 | 26-Mar-14 | 27-Mar-14 | -15 |
| P27-2012 | Place / Finish Deck | 0 | 0 | 28-Mar-14 | | -15 |

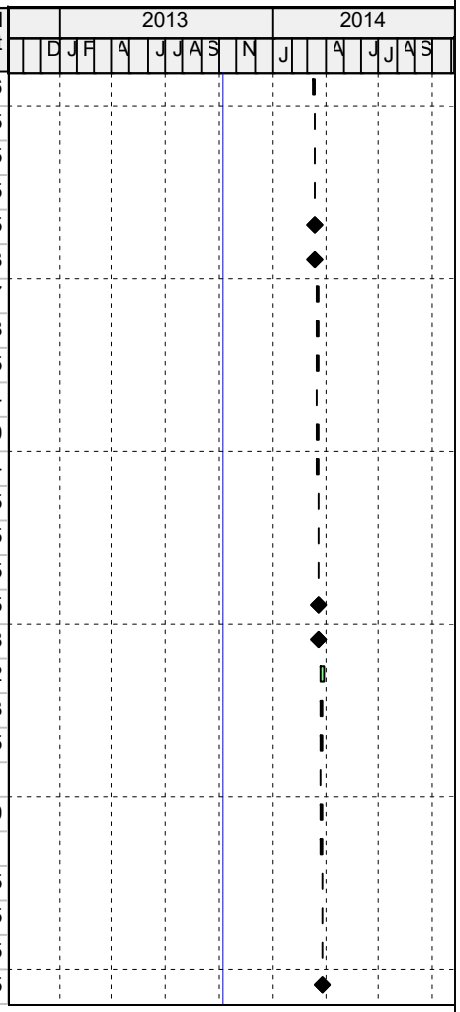



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P27-2020 | Place Conc @ Core | 0 | 0 | 28-Mar-14 | | 153 |
| P27-2014 | Stress Tendons | 1 | 1 | 31-Mar-14 | 31-Mar-14 | -2 |
| P28-2002 | FRP Columns Below | 5 | 5 | 31-Mar-14 | 04-Apr-14 | 147 |
| P28-2000 | Jump/Resteel/Close Core | 9 | 9 | 31-Mar-14 | 10-Apr-14 | -15 |
| P28-2004 | Shore / Form Deck | 6 | 6 | 31-Mar-14 | 07-Apr-14 | -15 |
| P23-2018 | Remove Reshores | 2 | 2 | 01-Apr-14 | 02-Apr-14 | 49 |
| P27-2016 | Strip / ReShore Deck | 3 | 3 | 01-Apr-14 | 03-Apr-14 | -2 |
| P28-2006 | MEP Rough In | 4 | 4 | 07-Apr-14 | 10-Apr-14 | -10 |
| P28-2008 | ReSteel / PT Cables | 4 | 4 | 07-Apr-14 | 10-Apr-14 | -10 |
| P28-2010 | Install Edgeform/Embeds | 2 | 2 | 07-Apr-14 | 08-Apr-14 | -8 |
| P28-2012 | Place / Finish Deck | 0 | 0 | 11-Apr-14 | | -10 |
| P28-2020 | Place Conc @ Core | 0 | 0 | 11-Apr-14 | | -15 |
| P29-2000 | Strip Core | 2 | 2 | 11-Apr-14 | 14-Apr-14 | -15 |
| P28-2014 | Stress Tendons | 1 | 1 | 14-Apr-14 | 14-Apr-14 | -10 |
| P24-2018 | Remove Reshores | 2 | 2 | 15-Apr-14 | 16-Apr-14 | 44 |
| P28-2016 | Strip / ReShore Deck | 3 | 3 | 15-Apr-14 | 17-Apr-14 | -10 |
| P29-2002 | FRP Columns Above Roof Deck | 3 | 3 | 15-Apr-14 | 17-Apr-14 | 138 |
| P29-2004 | Shore / Form Deck | 2 | 2 | 15-Apr-14 | 16-Apr-14 | -15 |
| P29-2006 | MEP Rough In | 1 | 1 | 16-Apr-14 | 16-Apr-14 | -15 |
| P29-2008 | ReSteel | 1 | 1 | 16-Apr-14 | 16-Apr-14 | -15 |
| P29-2010 | Install Edgeform/Embeds | 1 | 1 | 16-Apr-14 | 16-Apr-14 | -15 |
| P29-2012 | Place / Finish Deck | 0 | 0 | 17-Apr-14 | | -15 |
| P25-2018 | Remove Reshores | 2 | 2 | 17-Apr-14 | 18-Apr-14 | -15 |
| P26-2018 | Remove Reshores | 2 | 2 | 21-Apr-14 | 22-Apr-14 | -15 |
| P27-2018 | Remove Reshores | 2 | 2 | 23-Apr-14 | 24-Apr-14 | -15 |
| P28-2018 | Remove Reshores | 2 | 2 | 25-Apr-14 | 28-Apr-14 | -15 |
| **Ballroom Catwalk & Roof** | | | | | | |

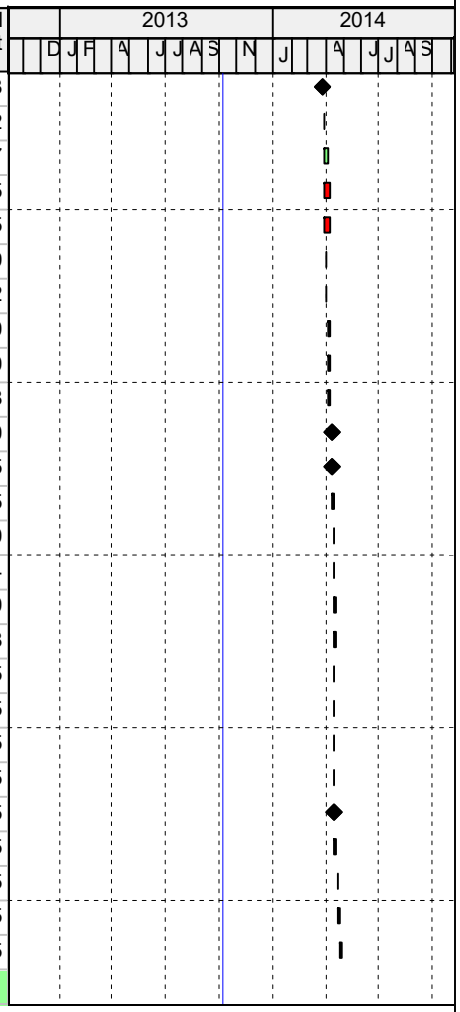



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PC-2100 | Erect Structural Steel @ Porte Cochere | 3 | 3 | 09-Jan-14 | 13-Jan-14 | -25 |
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 10 | 10 | 14-Jan-14 | 27-Jan-14 | -25 |
| PC-2102 | Metal Decking @ Ballroom Catwalk / Roof | 2 | 2 | 14-Jan-14 | 15-Jan-14 | 18 |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 3 | 28-Jan-14 | 30-Jan-14 | -25 |
| BR-2112 | BR - Fireproofing @ Structural Steel | 5 | 5 | 14-Feb-14 | 20-Feb-14 | 10 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Mech Penthouse** | | | | | | |
| PH-8702 | PH - Structural Steel / Decking / Framing | 10 | 10 | 24-Apr-14 | 07-May-14 | 30 |
| PH-8706 | Set Mech Equipment @ Tower Roof | 2 | 2 | 08-May-14 | 09-May-14 | 58 |
| PH-8708 | Set Equipment @ Penthouse | 3 | 3 | 08-May-14 | 12-May-14 | 57 |
| PH-8700 | High Roof - Structural Steel | 10 | 10 | 13-May-14 | 27-May-14 | 82 |
| **Vertical Circulation** | | | | | | |
| **Stairs** | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 1 | 1 | 04-Dec-13 | 04-Dec-13 | 137 |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 1 | 1 | 05-Dec-13 | 05-Dec-13 | 137 |
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 1 | 1 | 06-Dec-13 | 06-Dec-13 | 137 |
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 1 | 1 | 09-Dec-13 | 09-Dec-13 | 137 |
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 1 | 1 | 10-Dec-13 | 10-Dec-13 | 137 |
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 1 | 1 | 11-Dec-13 | 11-Dec-13 | 137 |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 1 | 1 | 12-Dec-13 | 12-Dec-13 | 137 |
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 1 | 1 | 13-Dec-13 | 13-Dec-13 | 137 |
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 1 | 1 | 16-Dec-13 | 16-Dec-13 | 137 |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 1 | 1 | 17-Dec-13 | 17-Dec-13 | 137 |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 1 | 1 | 18-Dec-13 | 18-Dec-13 | 137 |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 1 | 1 | 19-Dec-13 | 19-Dec-13 | 137 |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 1 | 1 | 20-Dec-13 | 20-Dec-13 | 137 |

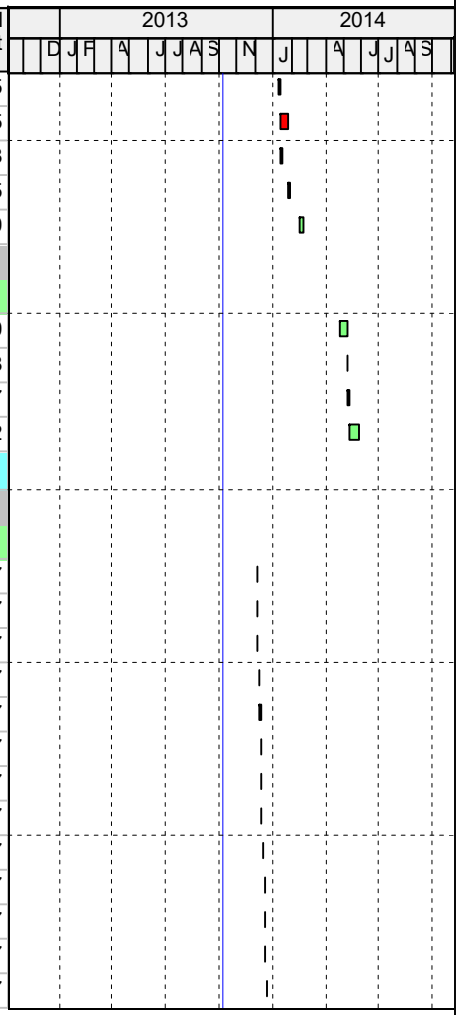



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 1 | 1 | 23-Dec-13 | 23-Dec-13 | 137 |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 1 | 1 | 24-Dec-13 | 24-Dec-13 | 137 |
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 1 | 1 | 26-Dec-13 | 26-Dec-13 | 137 |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 1 | 1 | 27-Dec-13 | 27-Dec-13 | 137 |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 1 | 1 | 30-Dec-13 | 30-Dec-13 | 137 |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 1 | 1 | 31-Dec-13 | 31-Dec-13 | 137 |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 1 | 1 | 02-Jan-14 | 02-Jan-14 | 137 |
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 1 | 1 | 04-Dec-13 | 04-Dec-13 | 133 |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 1 | 1 | 05-Dec-13 | 05-Dec-13 | 133 |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 1 | 1 | 06-Dec-13 | 06-Dec-13 | 133 |
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 1 | 1 | 20-Jan-14 | 20-Jan-14 | 106 |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 1 | 1 | 21-Jan-14 | 21-Jan-14 | 106 |
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 1 | 1 | 22-Jan-14 | 22-Jan-14 | 106 |
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 1 | 1 | 23-Jan-14 | 23-Jan-14 | 106 |
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 1 | 1 | 24-Jan-14 | 24-Jan-14 | 106 |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 1 | 1 | 27-Jan-14 | 27-Jan-14 | 106 |
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 1 | 1 | 28-Jan-14 | 28-Jan-14 | 106 |
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 1 | 1 | 29-Jan-14 | 29-Jan-14 | 106 |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 1 | 1 | 30-Jan-14 | 30-Jan-14 | 106 |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 1 | 1 | 31-Jan-14 | 31-Jan-14 | 106 |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 1 | 1 | 03-Feb-14 | 03-Feb-14 | 106 |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 1 | 1 | 04-Feb-14 | 04-Feb-14 | 106 |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 1 | 1 | 05-Feb-14 | 05-Feb-14 | 106 |
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 1 | 1 | 06-Feb-14 | 06-Feb-14 | 106 |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 1 | 1 | 07-Feb-14 | 07-Feb-14 | 106 |
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 1 | 1 | 10-Feb-14 | 10-Feb-14 | 106 |

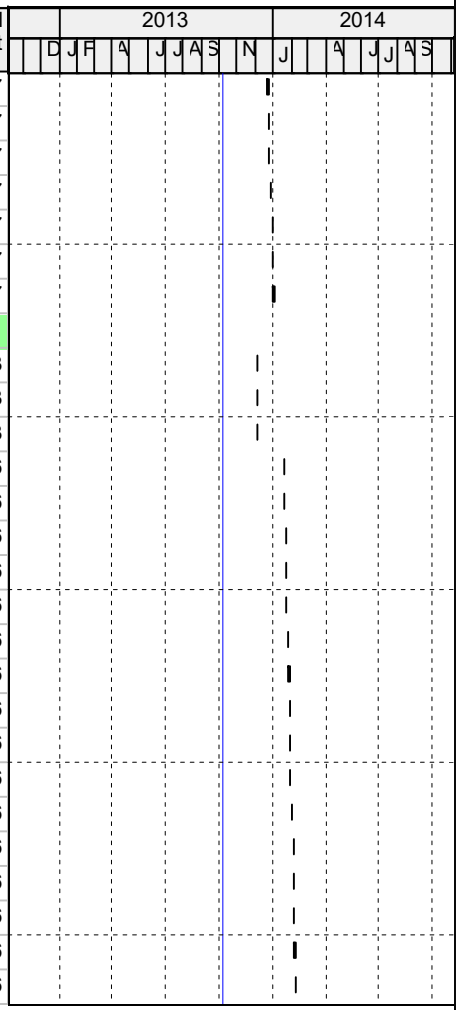



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - FRP Stairs LL2 | 6 | 6 | 04-Dec-13 | 11-Dec-13 | 7 |
| S3-4002 | Stair 3 - FRP Stairs LL1 | 6 | 6 | 12-Dec-13 | 19-Dec-13 | 7 |
| S3-4004 | Stair 3 - Permanent Railings / Final Finishes | 4 | 4 | 20-Dec-13 | 26-Dec-13 | 216 |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |
| S4-4000 | Stair 4 - FRP Stairs LL2 | 6 | 6 | 04-Dec-13 | 11-Dec-13 | 7 |
| S4-4002 | Stair 4 - FRP Stairs LL1 | 6 | 6 | 12-Dec-13 | 19-Dec-13 | 7 |
| S4-4004 | Stair 4 - FRP Stairs L1 | 6 | 6 | 16-Jan-14 | 23-Jan-14 | -5 |
| S4-4006 | Stair 4 - Permanent Railings / Final Finishes | 4 | 4 | 24-Jan-14 | 29-Jan-14 | 194 |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |
| S6-4000 | Stair 6 - FRP Stairs | 5 | 5 | 14-Jan-14 | 20-Jan-14 | -12 |
| S6-4002 | Stair 6 - Permanent Railings / Final Finishes | 2 | 2 | 21-Jan-14 | 22-Jan-14 | 199 |
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 4 | 14-Jan-14 | 17-Jan-14 | 106 |
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 10 | 21-Jan-14 | 03-Feb-14 | -12 |
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes | 5 | 5 | 04-Feb-14 | 10-Feb-14 | 186 |
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a - FRP Stairs L1 | 5 | 5 | 16-Jan-14 | 22-Jan-14 | -4 |
| S4a-4002 | Stair 4a - Permanent Railings / Final Finishes | 2 | 2 | 23-Jan-14 | 24-Jan-14 | 197 |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 07-Jun-13 A | | |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 0 | 17-Jun-13 A | 21-Jun-13 A | |
| EL-1004 | Elev - Submittal Approval | 21 | 1 | 21-Jun-13 A | 06-Oct-13 | 128 |
| EL-1006 | Elev - Release to Manufacturing | 14 | 14 | 07-Oct-13 | 20-Oct-13 | 128 |
| EL-1008 | Elev - Fabrication (Engineered Geared) | 120 | 120 | 21-Oct-13 | 17-Feb-14 | 128 |
| EL-1010 | Elev - Deliver to Jobsite | 1 | 1 | 18-Feb-14 | 18-Feb-14 | 91 |

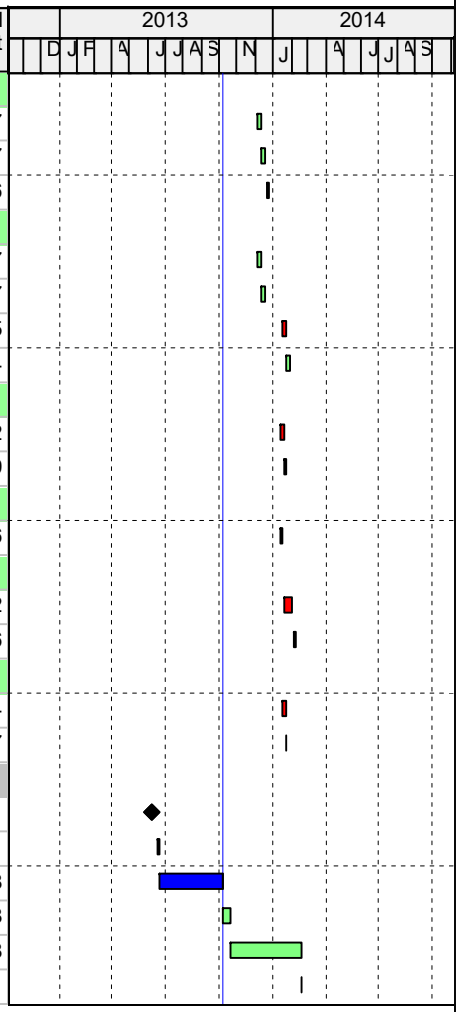



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Passenger Elevators 1-2 - LL2 to 17 - (18 Floors)** | | | | | | |
| EL-1202 | Elev 1/2 - Mob / Unload & Stage Equip / Materials | 5 | 5 | 19-Feb-14 | 25-Feb-14 | 91 |
| EL-1200 | Elev 1/2 - Hoistway Clear & Ready (GC) | 0 | 0 | 15-May-14 | | 35 |
| EL-1204 | Elev 1/2 - Install Rails & Brackets | 14 | 14 | 15-May-14 | 04-Jun-14 | 35 |
| EL-1206 | Elev 1/2 - Enclosed Mech Room w/ Power (GC) | 0 | 0 | | 04-Jun-14 | 35 |
| EL-1208 | Elev 1/2 - Install Machine & Controller | 10 | 10 | 05-Jun-14 | 18-Jun-14 | 35 |
| EL-1210 | Elev 1/2 - Install Pit Equip / Car Sling / Cwt Frame / W | 6 | 6 | 19-Jun-14 | 26-Jun-14 | 35 |
| EL-1212 | Elev 1/2 - Install Hoist & Cable | 5 | 5 | 27-Jun-14 | 03-Jul-14 | 35 |
| EL-1214 | Elev 1/2 - Install Entrances / Doors / Fixtures / Fascia | 15 | 15 | 07-Jul-14 | 25-Jul-14 | 35 |
| EL-1216 | Elev 1/2 - Complete Hoistway Walls (GC) | 0 | 0 | | 25-Jul-14 | 35 |
| EL-1218 | Elev 1/2 - Install Hoistway Equipment / Pipe & Wire | 10 | 10 | 14-Aug-14 | 27-Aug-14 | 22 |
| EL-1220 | Elev 1/2 - Install Cab / Wiring / Door Operators | 10 | 10 | 28-Aug-14 | 11-Sep-14 | 22 |
| EL-1222 | Elev 1/2 - Adjust | 8 | 8 | 12-Sep-14 | 23-Sep-14 | 22 |
| EL-1224 | Elev 1/2 - Clean / Paint / Punchlist | 4 | 4 | 24-Sep-14 | 29-Sep-14 | 22 |
| EL-1226 | Elev 1/2 - Inspections | 2 | 2 | 30-Sep-14 | 01-Oct-14 | 22 |
| **Passenger Elevators 3-4 - LL4 to 17 - (20 Floors)** | | | | | | |
| EL-3400 | Elev 3/4 - Hoistway Clear & Ready (GC) | 0 | 0 | 15-May-14 | | 30 |
| EL-3402 | Elev 3/4 - Mob / Unload & Stage Equip / Materials | 5 | 5 | 15-May-14 | 21-May-14 | 30 |
| EL-3404 | Elev 3/4 - Install Rails & Brackets | 14 | 14 | 22-May-14 | 11-Jun-14 | 30 |
| EL-3406 | Elev 3/4 - Enclosed Mech Room w/ Power (GC) | 0 | 0 | | 11-Jun-14 | 30 |
| EL-3408 | Elev 3/4 - Install Machine & Controller | 10 | 10 | 12-Jun-14 | 25-Jun-14 | 30 |
| EL-3410 | Elev 3/4 - Install Pit Equip / Car Sling / Cwt Frame / W | 6 | 6 | 26-Jun-14 | 03-Jul-14 | 30 |
| EL-3412 | Elev 3/4 - Install Hoist & Cable | 5 | 5 | 07-Jul-14 | 11-Jul-14 | 30 |
| EL-3414 | Elev 3/4 - Install Entrances / Doors / Fixtures / Fascia | 15 | 15 | 14-Jul-14 | 01-Aug-14 | 30 |
| EL-3416 | Elev 3/4 - Complete Hoistway Walls (GC) | 0 | 0 | | 01-Aug-14 | 30 |
| EL-3418 | Elev 3/4 - Install Hoistway Equipment / Pipe & Wire | 10 | 10 | 04-Aug-14 | 15-Aug-14 | 30 |
| EL-3420 | Elev 3/4 - Install Cab / Wiring / Door Operators | 10 | 10 | 18-Aug-14 | 29-Aug-14 | 30 |

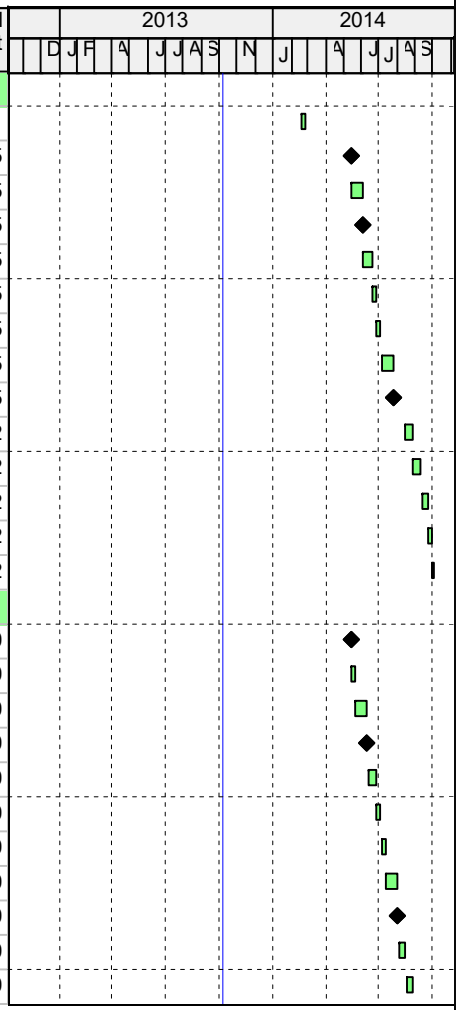



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-3422 | Elev 3/4 - Adjust | 8 | 8 | 02-Sep-14 | 11-Sep-14 | 30 |
| EL-3424 | Elev 3/4 - Clean / Paint / Punchlist | 4 | 4 | 12-Sep-14 | 17-Sep-14 | 30 |
| EL-3426 | Elev 3/4 - Inspections | 2 | 2 | 18-Sep-14 | 19-Sep-14 | 30 |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 5 | 5 | 08-May-14 | 14-May-14 | 31 |
| EL-5016 | Elev 5 - Complete Hoistway Walls (GC) | 0 | 0 | | 14-May-14 | 80 |
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 15-May-14 | | 31 |
| EL-5004 | Elev 5 - Install Rails & Brackets | 15 | 15 | 15-May-14 | 05-Jun-14 | 31 |
| EL-5018 | Elev 5 - Install Machine Room Equipment | 5 | 5 | 15-May-14 | 21-May-14 | 80 |
| EL-5020 | Elev 5 - Install Cab / Wiring / Door Operators | 10 | 10 | 22-May-14 | 05-Jun-14 | 80 |
| EL-5006 | Elev 5 - Enclosed Mech Room w/ Power (GC) | 0 | 0 | | 05-Jun-14 | 31 |
| EL-5008 | Elev 5 - Install Machine & Controller | 10 | 10 | 06-Jun-14 | 19-Jun-14 | 31 |
| EL-5010 | Elev 5 - Install Pit Equip / Car Sling / Cwt Frame / Wei | 5 | 5 | 20-Jun-14 | 26-Jun-14 | 31 |
| EL-5012 | Elev 5 - Install Hoist & Cable | 12 | 12 | 27-Jun-14 | 15-Jul-14 | 31 |
| EL-5014 | Elev 5 - Install Entrances / Doors / Fixtures / Fascia | 22 | 22 | 16-Jul-14 | 14-Aug-14 | 31 |
| EL-5022 | Elev 5 - Adjust | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 31 |
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 4 | 4 | 22-Aug-14 | 27-Aug-14 | 31 |
| EL-5026 | Elev 5 - Inspections | 2 | 2 | 28-Aug-14 | 29-Aug-14 | 44 |
| **Service Elevator 6 - LL2 to 1 - (3 Floors)** | | | | | | |
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 15-May-14 | | 58 |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 3 | 3 | 15-May-14 | 19-May-14 | 58 |
| EL-6004 | Elev 6 - Install Rails & Brackets | 10 | 10 | 20-May-14 | 03-Jun-14 | 58 |
| EL-6006 | Elev 6 - Enclosed Mech Room w/ Power (GC) | 0 | 0 | | 03-Jun-14 | 58 |
| EL-6008 | Elev 6 - Install Machine & Controller | 10 | 10 | 04-Jun-14 | 17-Jun-14 | 58 |
| EL-6010 | Elev 6 - Install Pit Equip / Car Sling / Cwt Frame / Wei | 5 | 5 | 18-Jun-14 | 24-Jun-14 | 58 |
| EL-6012 | Elev 6 - Install Hoist & Cable | 3 | 3 | 25-Jun-14 | 27-Jun-14 | 58 |
| EL-6014 | Elev 6 - Install Entrances / Doors / Fixtures / Fascia | 10 | 10 | 30-Jun-14 | 14-Jul-14 | 58 |

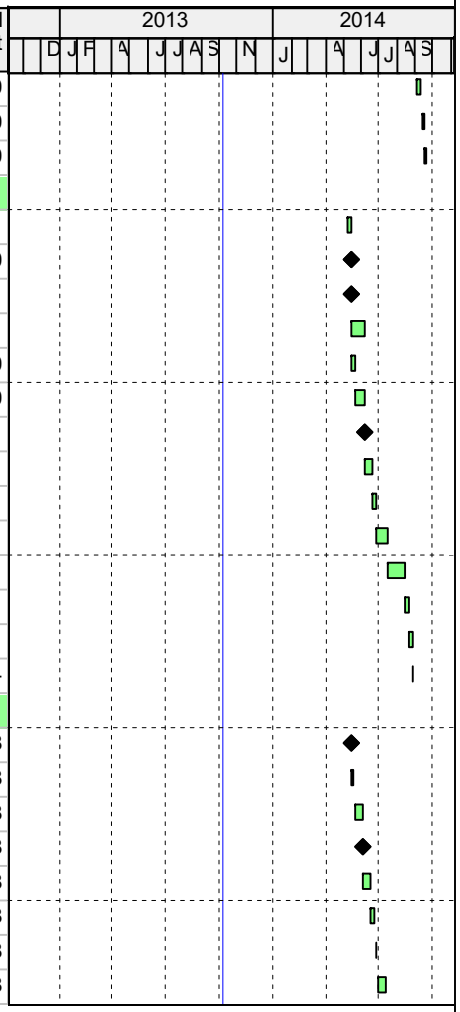



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6016 | Elev 6 - Complete Hoistway Walls (GC) | 0 | 0 | | 14-Jul-14 | 58 |
| EL-6018 | Elev 6 - Install Hoistway Equipment / Pipe & Wire | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 58 |
| EL-6020 | Elev 6 - Install Cab / Wiring / Door Operators | 5 | 5 | 22-Jul-14 | 28-Jul-14 | 58 |
| EL-6022 | Elev 6 - Adjust | 5 | 5 | 29-Jul-14 | 04-Aug-14 | 58 |
| EL-6024 | Elev 6 - Clean / Paint / Punchlist | 3 | 3 | 05-Aug-14 | 07-Aug-14 | 58 |
| EL-6026 | Elev 6 - Inspections | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 58 |
| **Exterior Shell** | | | | | | |
| **Elevations** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2** | | | | | | |
| LL1-5308 | LL1 Thru L4 - Support Frame/Sheathing for Metal Wa | 10 | 10 | 16-Jan-14 | 29-Jan-14 | 194 |
| L1-5308 | L1 - Support Frame/Sheathing for Metal Wall Panels | 9 | 9 | 24-Jan-14 | 05-Feb-14 | -14 |
| LL2-5308 | LL2 Thru L4 - Support Frame/Sheathing for Metal Wa | 10 | 10 | 06-Feb-14 | 19-Feb-14 | 134 |
| L3-5308 | L3- Support Frame/Sheathing for Metal Wall Panels | 9 | 9 | 06-Feb-14 | 18-Feb-14 | 34 |
| L4-5308 | L4- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 13-Feb-14 | 19-Feb-14 | 43 |
| LL2-5116 | LL2 Thru L4 - Metal Wall Panels (East/North) | 10 | 10 | 20-Feb-14 | 05-Mar-14 | 134 |
| L5-5308 | L5- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 20-Feb-14 | 26-Feb-14 | 43 |
| L6-5308 | L6- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 27-Feb-14 | 05-Mar-14 | 75 |
| L7-5308 | L7- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 06-Mar-14 | 12-Mar-14 | 154 |
| L8-5308 | L8- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 13-Mar-14 | 19-Mar-14 | 70 |
| L9-5308 | L9- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 20-Mar-14 | 26-Mar-14 | 70 |
| L10-5308 | L10- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 27-Mar-14 | 02-Apr-14 | 70 |
| L11-5308 | L11- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 03-Apr-14 | 09-Apr-14 | 70 |
| L12-5308 | L12- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 17-Apr-14 | 23-Apr-14 | 65 |
| L14-5308 | L14 - Support Frame/Sheathing for Metal Wall Panel | 5 | 5 | 21-Apr-14 | 25-Apr-14 | 81 |
| L15-5308 | L15 - Support Frame/Sheathing for Metal Wall Panel | 5 | 5 | 23-Apr-14 | 29-Apr-14 | 84 |
| L16-5308 | L16- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 25-Apr-14 | 01-May-14 | 87 |

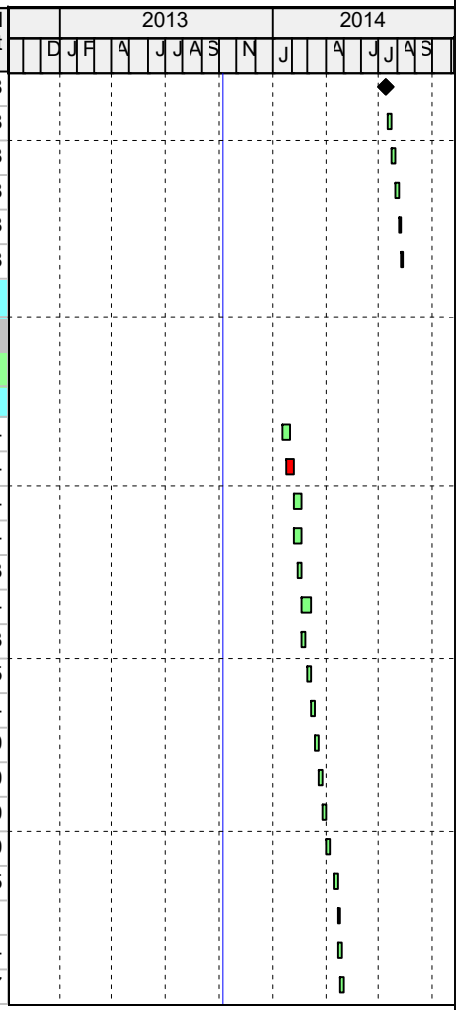



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-5308 | L17 - Support Frame/Sheathing for Metal Wall Panel | 5 | 5 | 29-Apr-14 | 05-May-14 | -15 |
| **Lower Level 1** | | | | | | |
| LL1-5116 | LL1 Thru L4 - Metal Wall Panels (East/North) | 10 | 10 | 06-Mar-14 | 19-Mar-14 | 134 |
| **Level 1** | | | | | | |
| L1-5116 | L1 - Metal Wall Panels | 10 | 10 | 20-Mar-14 | 02-Apr-14 | 134 |
| L7-5116 | L7 - Metal Wall Panels | 5 | 5 | 20-Mar-14 | 26-Mar-14 | 154 |
| L1-5102 | L1 - Storefront Frames | 10 | 10 | 03-Apr-14 | 16-Apr-14 | 134 |
| L1-5104 | L1 - Storefront Glazing | 5 | 5 | 17-Apr-14 | 23-Apr-14 | 134 |
| EP-5110 | L1 - Revolving Doors | 5 | 5 | 17-Apr-14 | 23-Apr-14 | 134 |
| L3-5116 | L3 - Metal Wall Panels | 10 | 10 | 06-May-14 | 19-May-14 | -15 |
| L3-5102 | L3- Storefront Frames | 10 | 10 | 20-May-14 | 03-Jun-14 | 101 |
| L4-5116 | L4 - Metal Wall Panels | 5 | 5 | 20-May-14 | 27-May-14 | -15 |
| L5-5116 | L5 - Metal Wall Panels | 5 | 5 | 28-May-14 | 03-Jun-14 | -15 |
| L3-5104 | L3 - Storefront Glazing | 5 | 5 | 04-Jun-14 | 10-Jun-14 | 101 |
| L6-5116 | L6 - Metal Wall Panels | 5 | 5 | 04-Jun-14 | 10-Jun-14 | 17 |
| L8-5116 | L8 - Metal Wall Panels | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 17 |
| L9-5116 | L9 - Metal Wall Panels | 5 | 5 | 18-Jun-14 | 24-Jun-14 | 17 |
| L10-5116 | L10 - Metal Wall Panels | 5 | 5 | 25-Jun-14 | 01-Jul-14 | 17 |
| L11-5116 | L11 - Metal Wall Panels | 5 | 5 | 02-Jul-14 | 09-Jul-14 | 17 |
| L12-5116 | L12 - Metal Wall Panels | 5 | 5 | 10-Jul-14 | 16-Jul-14 | 17 |
| L14-5116 | L14 - Metal Wall Panels | 5 | 5 | 17-Jul-14 | 23-Jul-14 | 30 |
| L15-5116 | L15 - Metal Wall Panels | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 30 |
| L16-5116 | L16 - Metal Wall Panels | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 30 |
| L17-5116 | L17 - Metal Wall Panels | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 30 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Levels 3-4** | | | | | | |
| L3-5130 | L3 - Install Punch Windows | 5 | 5 | 19-Feb-14 | 25-Feb-14 | 34 |

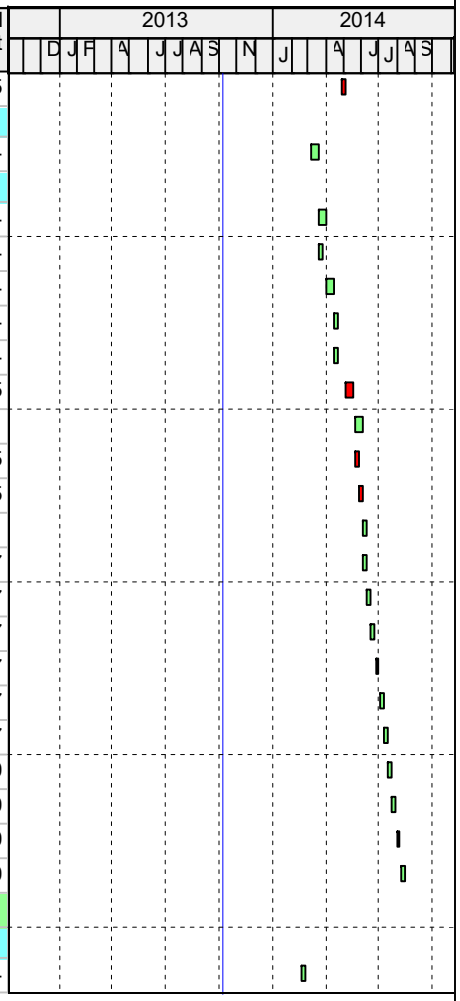



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L4-5130 | L4 - Install Punch Windows | 5 | 5 | 20-Feb-14 | 26-Feb-14 | 43 |
| L5-5130 | L5 - Install Punch Windows | 5 | 5 | 27-Feb-14 | 05-Mar-14 | 43 |
| L6-5130 | L6- Install Punch Windows | 5 | 5 | 06-Mar-14 | 12-Mar-14 | 75 |
| L7-5130 | L7 - Install Punch Windows | 5 | 5 | 13-Mar-14 | 19-Mar-14 | 154 |
| L8-5130 | L8 - Install Punch Windows | 5 | 5 | 20-Mar-14 | 26-Mar-14 | 70 |
| L9-5130 | L9 - Install Punch Windows | 5 | 5 | 27-Mar-14 | 02-Apr-14 | 70 |
| L10-5130 | L10 - Install Punch Windows | 5 | 5 | 03-Apr-14 | 09-Apr-14 | 70 |
| L11-5130 | L11 - Install Punch Windows | 5 | 5 | 10-Apr-14 | 16-Apr-14 | 70 |
| L12-5130 | L12 - Install Punch Windows | 5 | 5 | 24-Apr-14 | 30-Apr-14 | 65 |
| L14-5130 | L14 - Install Punch Windows | 5 | 5 | 28-Apr-14 | 02-May-14 | 81 |
| L15-5130 | L15 - Install Punch Windows | 5 | 5 | 30-Apr-14 | 06-May-14 | 84 |
| L16-5130 | L16 - Install Punch Windows | 5 | 5 | 02-May-14 | 08-May-14 | 87 |
| L17-5130 | L17 - Install Punch Windows | 5 | 5 | 06-May-14 | 12-May-14 | 90 |
| Roofs | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 5 | 16-Jan-14 | 22-Jan-14 | -15 |
| RF-4026 | L1 - City Park - Protection Board | 3 | 3 | 23-Jan-14 | 27-Jan-14 | 194 |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 2 | 28-Jan-14 | 29-Jan-14 | 194 |
| **Pool Membrane - (elev 18')** | | | | | | |
| RF-4034 | Pool Waterproofing / Membrane | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 30 |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 15 | 15 | 14-Feb-14 | 06-Mar-14 | -25 |
| RF-4010 | AR - Set Mechanical Equipment | 5 | 5 | 07-Mar-14 | 13-Mar-14 | -25 |
| RF-4012 | AR - Coping / Flashing | 4 | 4 | 07-Mar-14 | 12-Mar-14 | 13 |
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 5 | 5 | 07-Mar-14 | 13-Mar-14 | -3 |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |

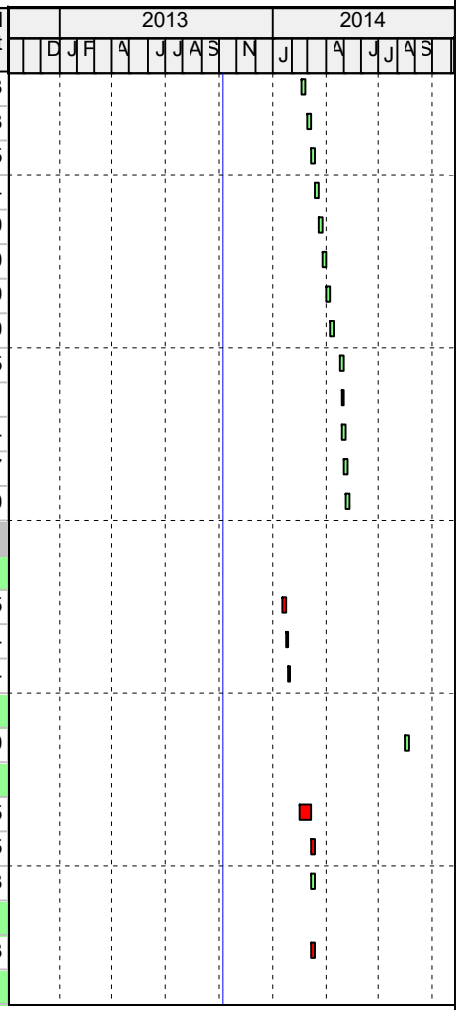



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PC-4008 | RF - Entry / Porte Cochere Roofing System | 15 | 15 | 14-Feb-14 | 06-Mar-14 | -3 |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | Rf - Upper Ballroom Roofing System | 10 | 10 | 31-Jan-14 | 13-Feb-14 | -24 |
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 10 | 10 | 04-Jun-14 | 17-Jun-14 | -15 |
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |
| RF-4018 | TR - Terrace Roof - Roofing System | 5 | 5 | 17-Jul-14 | 23-Jul-14 | 17 |
| RF-4020 | TR - Terrace Roof - Coping / Flashing | 3 | 3 | 24-Jul-14 | 28-Jul-14 | 68 |
| RF-4022 | TR - Terrace Roof - Glass Railing | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 17 |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Substrates / Land Mech | 20 | 20 | 28-May-14 | 24-Jun-14 | 82 |
| RF-4002 | Tower Roof - Roofing / Roof Structures | 18 | 18 | 11-Jun-14 | 07-Jul-14 | 82 |
| **PH - Roof - (elev 173')** | | | | | | |
| RF-4030 | PH - Roofing System | 5 | 5 | 08-May-14 | 14-May-14 | 30 |
| RF-4032 | PH - Coping / Flashing | 2 | 2 | 15-May-14 | 16-May-14 | 117 |
| **Rough-In's** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6002 | LL4 - Layout | 1 | 1 | 12-Nov-13 | 12-Nov-13 | 110 |
| LL4-6004 | LL4 - CMU Walls | 5 | 5 | 13-Nov-13 | 19-Nov-13 | 110 |
| LL4-6008 | LL4 - Int Wall Framing | 5 | 5 | 20-Nov-13 | 26-Nov-13 | 110 |
| LL4-6010 | LL4 - F/P Curbs | 5 | 5 | 20-Nov-13 | 26-Nov-13 | 120 |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 2 | 20-Nov-13 | 21-Nov-13 | 123 |
| LL4-6012 | LL4 - Fire Sprinkler RI | 10 | 10 | 27-Nov-13 | 12-Dec-13 | 110 |
| LL4-6014 | LL4 - Plumbing RI | 10 | 10 | 27-Nov-13 | 12-Dec-13 | 110 |
| LL4-6016 | LL4 - Electrical RI | 10 | 10 | 27-Nov-13 | 12-Dec-13 | 110 |
| LL4-6018 | LL4 - HVAC RI | 10 | 10 | 27-Nov-13 | 12-Dec-13 | 110 |

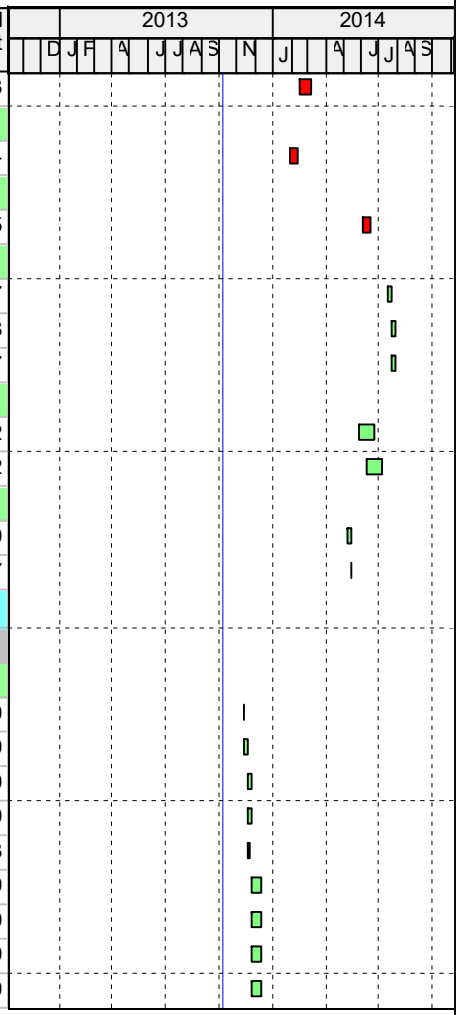



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-6020 | LL4 - H Mtl Frames | 3 | 3 | 27-Nov-13 | 03-Dec-13 | 117 |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties RI | 8 | 8 | 27-Nov-13 | 10-Dec-13 | 144 |
| LL4-6024 | LL4 - Inspections | 2 | 2 | 13-Dec-13 | 16-Dec-13 | 110 |
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6002 | LL3 - Layout | 1 | 1 | 04-Dec-13 | 04-Dec-13 | 97 |
| LL3-6004 | LL3 - CMU Walls | 5 | 5 | 05-Dec-13 | 11-Dec-13 | 97 |
| LL3-6008 | LL3 - Int Wall Framing | 5 | 5 | 12-Dec-13 | 18-Dec-13 | 97 |
| LL3-6010 | LL3 - F/P Curbs | 5 | 5 | 12-Dec-13 | 18-Dec-13 | 107 |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 2 | 12-Dec-13 | 13-Dec-13 | 110 |
| LL3-6012 | LL3 - Fire Sprinkler RI | 10 | 10 | 19-Dec-13 | 03-Jan-14 | 97 |
| LL3-6014 | LL3 - Plumbing RI | 10 | 10 | 19-Dec-13 | 03-Jan-14 | 97 |
| LL3-6016 | LL3 - Electrical RI | 10 | 10 | 19-Dec-13 | 03-Jan-14 | 97 |
| LL3-6018 | LL3 - HVAC RI | 10 | 10 | 19-Dec-13 | 03-Jan-14 | 97 |
| LL3-6020 | LL3 - H Mtl Frames | 3 | 3 | 19-Dec-13 | 23-Dec-13 | 104 |
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties RI | 8 | 8 | 19-Dec-13 | 31-Dec-13 | 135 |
| LL3-6024 | LL3 - Inspections | 2 | 2 | 06-Jan-14 | 07-Jan-14 | 97 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6002 | LL2 - Layout | 1 | 1 | 31-Dec-13 | 31-Dec-13 | 67 |
| LL2-6004 | LL2 - CMU Walls | 18 | 18 | 02-Jan-14 | 28-Jan-14 | 67 |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 3 | 02-Jan-14 | 06-Jan-14 | 80 |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 2 | 2 | 07-Jan-14 | 08-Jan-14 | 80 |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 5 | 29-Jan-14 | 04-Feb-14 | 67 |
| LL2-6010 | LL2 - F/P Curbs @ Parking | 5 | 5 | 29-Jan-14 | 04-Feb-14 | 129 |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 4 | 29-Jan-14 | 03-Feb-14 | 78 |
| LL2-6012 | LL2 - Fire Sprinkler RI | 10 | 10 | 05-Feb-14 | 18-Feb-14 | 67 |
| LL2-6014 | LL2 - Plumbing RI | 10 | 10 | 05-Feb-14 | 18-Feb-14 | 67 |
| LL2-6016 | LL2 - Electrical RI | 10 | 10 | 05-Feb-14 | 18-Feb-14 | 67 |

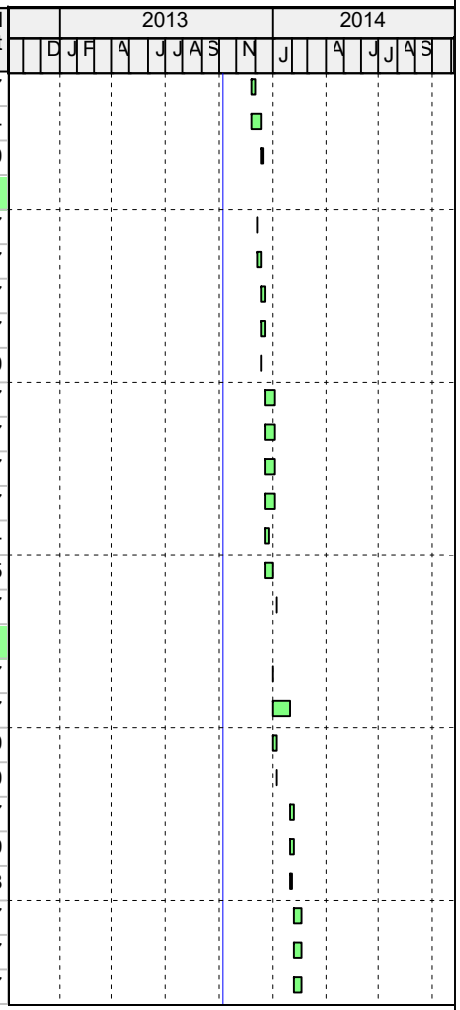



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-6018 | LL2 - HVAC RI | 10 | 10 | 05-Feb-14 | 18-Feb-14 | 67 |
| LL2-6020 | LL2 - H Mtl Frames | 3 | 3 | 05-Feb-14 | 07-Feb-14 | 74 |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties RI | 8 | 8 | 05-Feb-14 | 14-Feb-14 | 98 |
| LL2-6024 | LL2 - Inspections | 2 | 2 | 19-Feb-14 | 20-Feb-14 | 67 |
| LL2-6015 | LL2 - Main Elect Room Set Equip / RI - Power to Ma | 40 | 40 | 18-Jun-14 | 13-Aug-14 | 16 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6002 | LL1 - Layout | 1 | 1 | 15-Jan-14 | 15-Jan-14 | -18 |
| LL1-6004 | LL1 - CMU Walls | 9 | 9 | 16-Jan-14 | 28-Jan-14 | -18 |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 3 | 16-Jan-14 | 20-Jan-14 | -15 |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 3 | 3 | 21-Jan-14 | 23-Jan-14 | -15 |
| LL1-6008 | LL1 - Int Wall Framing | 15 | 15 | 29-Jan-14 | 18-Feb-14 | -18 |
| LL1-6010 | LL1 - CMU Seismic Clips | 2 | 2 | 29-Jan-14 | 30-Jan-14 | 25 |
| LL1-6012 | LL1 - Fire Sprinkler RI | 14 | 14 | 19-Feb-14 | 10-Mar-14 | -2 |
| LL1-6014 | LL1 - Plumbing RI | 15 | 15 | 19-Feb-14 | 11-Mar-14 | -3 |
| LL1-6016 | LL1 - Electrical RI | 25 | 25 | 19-Feb-14 | 25-Mar-14 | -13 |
| LL1-6018 | LL1 - HVAC RI | 30 | 30 | 19-Feb-14 | 01-Apr-14 | -18 |
| LL1-6020 | LL1 - H Mtl Frames | 5 | 5 | 19-Feb-14 | 25-Feb-14 | 7 |
| LL1-6022 | LL1 - Fire Alarm / Elec Specialties RI | 10 | 10 | 19-Feb-14 | 04-Mar-14 | 46 |
| LL1-6024 | LL1 - Inspections | 2 | 2 | 02-Apr-14 | 03-Apr-14 | -18 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-6002 | L1 - Layout | 1 | 1 | 16-Jan-14 | 16-Jan-14 | -13 |
| L01-6004 | L1 - CMU Walls | 8 | 8 | 17-Jan-14 | 28-Jan-14 | -8 |
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 5 | 17-Jan-14 | 23-Jan-14 | -13 |
| L01-6010 | L1 - CMU Seismic Clips | 1 | 1 | 29-Jan-14 | 29-Jan-14 | 36 |
| L01-6008 | L1 - Int Wall Framing | 15 | 15 | 06-Feb-14 | 26-Feb-14 | -14 |
| L01-6012 | L1 - Fire Sprinkler RI | 14 | 14 | 27-Feb-14 | 18-Mar-14 | 2 |

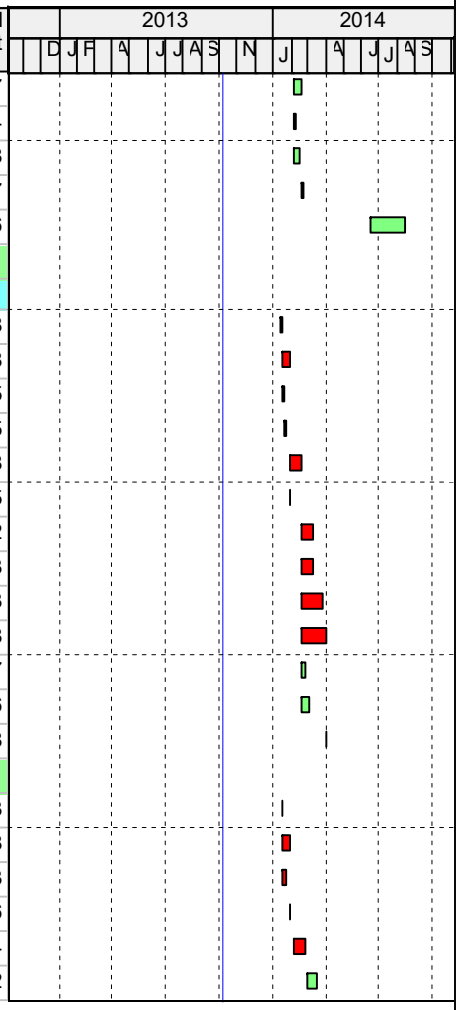



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L01-6014 | L1 - Plumbing RI | 20 | 20 | 27-Feb-14 | 26-Mar-14 | -4 |
| L01-6016 | L1 - Electrical RI | 25 | 25 | 27-Feb-14 | 02-Apr-14 | -9 |
| L01-6020 | L1 - H Mtl Frames | 5 | 5 | 27-Feb-14 | 05-Mar-14 | 11 |
| L01-6022 | L1 - Fire Alarm / Elec Specialties RI | 10 | 10 | 27-Feb-14 | 12-Mar-14 | 42 |
| L01-6018 | L1 - HVAC RI | 30 | 30 | 14-Mar-14 | 24-Apr-14 | -25 |
| L01-6024 | L1 - Inspections | 2 | 2 | 25-Apr-14 | 28-Apr-14 | -25 |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6002 | L2 - Layout | 1 | 1 | 30-Jan-14 | 30-Jan-14 | -2 |
| L02-6004 | L2 - CMU Walls | 5 | 5 | 31-Jan-14 | 06-Feb-14 | 8 |
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 5 | 31-Jan-14 | 06-Feb-14 | -2 |
| L02-6006 | L2 - Ext Wall Framing - (Cold Formed) | 10 | 10 | 07-Feb-14 | 20-Feb-14 | -2 |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 1 | 07-Feb-14 | 07-Feb-14 | 44 |
| L02-6008 | L2 - Int Wall Framing | 12 | 12 | 21-Feb-14 | 10-Mar-14 | -2 |
| L02-6012 | L2 - Fire Sprinkler RI | 10 | 10 | 11-Mar-14 | 24-Mar-14 | 13 |
| L02-6014 | L2 - Plumbing RI | 12 | 12 | 11-Mar-14 | 26-Mar-14 | 11 |
| L02-6016 | L2 - Electrical RI | 20 | 20 | 11-Mar-14 | 07-Apr-14 | 3 |
| L02-6018 | L2 - HVAC RI | 25 | 25 | 11-Mar-14 | 14-Apr-14 | -2 |
| L02-6020 | L2 - H Mtl Frames | 5 | 5 | 11-Mar-14 | 17-Mar-14 | 10 |
| L02-6022 | L2 - Fire Alarm / Elec Specialties RI | 10 | 10 | 11-Mar-14 | 24-Mar-14 | 38 |
| L02-6024 | L2 - Inspections | 2 | 2 | 15-Apr-14 | 16-Apr-14 | -2 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L03-6002 | L3 - Layout | 1 | 1 | 06-Feb-14 | 06-Feb-14 | 30 |
| L03-6004 | L3 - CMU Wall | 5 | 5 | 07-Feb-14 | 13-Feb-14 | 30 |
| L03-6008 | L3 - Int Wall Framing | 5 | 5 | 14-Feb-14 | 20-Feb-14 | 30 |
| L03-6010 | L3 - CMU Seismic Clips | 1 | 1 | 14-Feb-14 | 14-Feb-14 | 44 |
| L03-6012 | L3 - Fire Sprinkler RI | 10 | 10 | 21-Feb-14 | 06-Mar-14 | 30 |

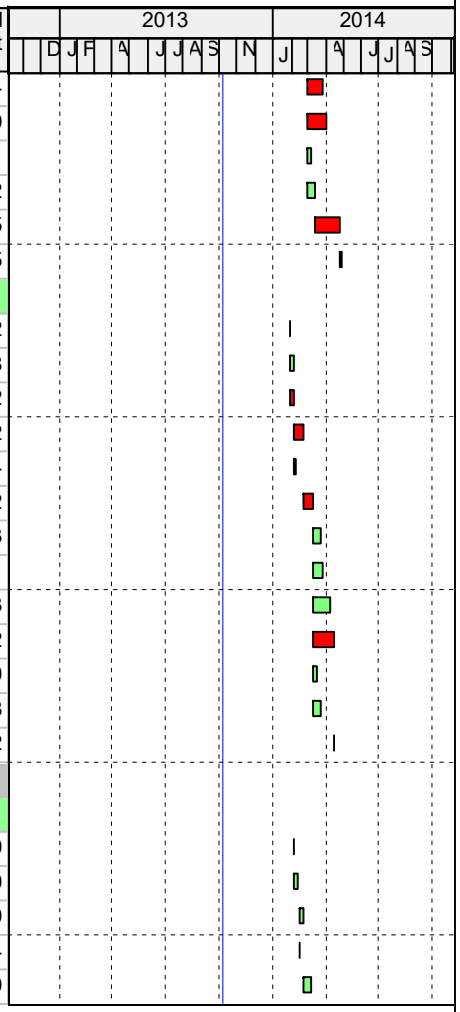



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6014 | L3 - Plumbing RI | 10 | 10 | 21-Feb-14 | 06-Mar-14 | 30 |
| L03-6016 | L3 - Electrical RI | 10 | 10 | 21-Feb-14 | 06-Mar-14 | 30 |
| L03-6018 | L3 - HVAC RI | 10 | 10 | 21-Feb-14 | 06-Mar-14 | 30 |
| L03-6020 | L3 - H Mtl Frames | 3 | 3 | 21-Feb-14 | 25-Feb-14 | 42 |
| L03-6022 | L3 - Fire Alarm / Elec Specialties RI | 8 | 8 | 21-Feb-14 | 04-Mar-14 | 57 |
| L03-6024 | L3 - Inspections | 2 | 2 | 07-Mar-14 | 10-Mar-14 | 30 |
| L03-6000 | L3 - Skim Ceiling | 4 | 4 | 14-Mar-14 | 19-Mar-14 | 37 |
| **Level 4 - (Guest Rooms)** | | | | | | |
| L04-6002 | L4 - Layout | 1 | 1 | 13-Feb-14 | 13-Feb-14 | 30 |
| L04-6004 | L4 - CMU Walls | 5 | 5 | 14-Feb-14 | 20-Feb-14 | 30 |
| L04-6008 | L4 - Int Wall Framing | 5 | 5 | 21-Feb-14 | 27-Feb-14 | 30 |
| L04-6010 | L4 - CMU Seismic Clips | 1 | 1 | 21-Feb-14 | 21-Feb-14 | 44 |
| L04-6012 | L4 - Fire Sprinkler RI | 10 | 10 | 28-Feb-14 | 13-Mar-14 | 30 |
| L04-6014 | L4 - Plumbing RI | 10 | 10 | 28-Feb-14 | 13-Mar-14 | 30 |
| L04-6016 | L4 - Electrical RI | 10 | 10 | 28-Feb-14 | 13-Mar-14 | 30 |
| L04-6018 | L4 - HVAC RI | 10 | 10 | 28-Feb-14 | 13-Mar-14 | 30 |
| L04-6020 | L4 - H Mtl Frames | 3 | 3 | 28-Feb-14 | 04-Mar-14 | 42 |
| L04-6022 | L4 - Fire Alarm / Elec Specialties RI | 8 | 8 | 28-Feb-14 | 11-Mar-14 | 57 |
| L04-6024 | L4 - Inspections | 2 | 2 | 14-Mar-14 | 17-Mar-14 | 30 |
| L04-6000 | L4 - Skim Ceiling | 4 | 4 | 21-Mar-14 | 26-Mar-14 | 37 |
| **Level 5 - (Guest Rooms)** | | | | | | |
| L05-6002 | L5 - Layout | 1 | 1 | 20-Feb-14 | 20-Feb-14 | 30 |
| L05-6004 | L5 - CMU Walls | 5 | 5 | 21-Feb-14 | 27-Feb-14 | 30 |
| L05-6008 | L5 - Int Wall Framing | 5 | 5 | 28-Feb-14 | 06-Mar-14 | 30 |
| L05-6010 | L5 - CMU Seismic Clips | 1 | 1 | 28-Feb-14 | 28-Feb-14 | 44 |
| L05-6012 | L5 - Fire Sprinkler RI | 10 | 10 | 07-Mar-14 | 20-Mar-14 | 30 |
| L05-6014 | L5 - Plumbing RI | 10 | 10 | 07-Mar-14 | 20-Mar-14 | 30 |

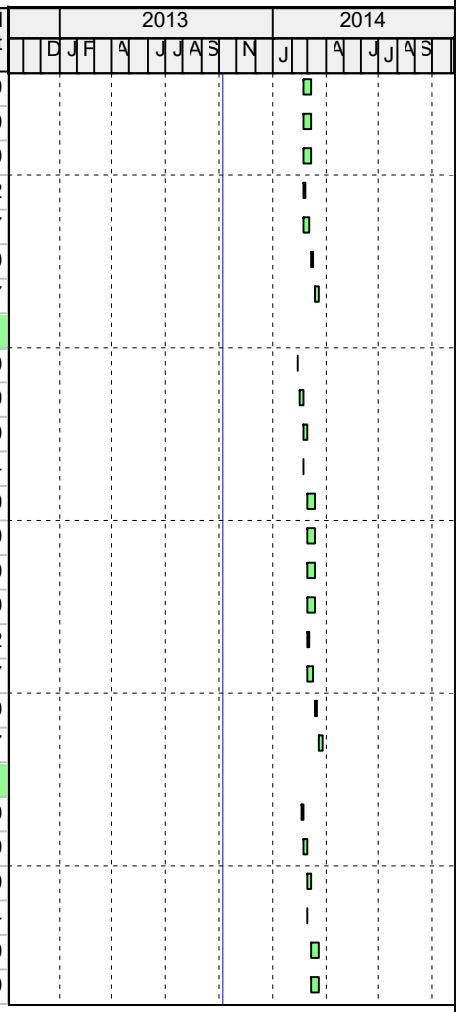



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6016 | L5 - Electrical RI | 10 | 10 | 07-Mar-14 | 20-Mar-14 | 30 |
| L05-6018 | L5 - HVAC RI | 10 | 10 | 07-Mar-14 | 20-Mar-14 | 30 |
| L05-6020 | L5 - H Mtl Frames | 3 | 3 | 07-Mar-14 | 11-Mar-14 | 42 |
| L05-6022 | L5 - Fire Alarm / Elec Specialties RI | 8 | 8 | 07-Mar-14 | 18-Mar-14 | 57 |
| L05-6024 | L5 - Inspections | 2 | 2 | 21-Mar-14 | 24-Mar-14 | 30 |
| L05-6000 | L5 - Skim Ceiling | 4 | 4 | 28-Mar-14 | 02-Apr-14 | 37 |
| **Level 6 - (Guest Rooms)** | | | | | | |
| L06-6002 | L6 - Layout | 1 | 1 | 27-Feb-14 | 27-Feb-14 | 30 |
| L06-6004 | L6 - CMU Walls | 5 | 5 | 28-Feb-14 | 06-Mar-14 | 30 |
| L06-6008 | L6 - Int Wall Framing | 5 | 5 | 07-Mar-14 | 13-Mar-14 | 30 |
| L06-6010 | L6 - CMU Seismic Clips | 1 | 1 | 07-Mar-14 | 07-Mar-14 | 44 |
| L06-6012 | L6 - Fire Sprinkler RI | 10 | 10 | 14-Mar-14 | 27-Mar-14 | 30 |
| L06-6014 | L6 - Plumbing RI | 10 | 10 | 14-Mar-14 | 27-Mar-14 | 30 |
| L06-6016 | L6 - Electrical RI | 10 | 10 | 14-Mar-14 | 27-Mar-14 | 30 |
| L06-6018 | L6 - HVAC RI | 10 | 10 | 14-Mar-14 | 27-Mar-14 | 30 |
| L06-6020 | L6 - H Mtl Frames | 3 | 3 | 14-Mar-14 | 18-Mar-14 | 42 |
| L06-6022 | L6 - Fire Alarm / Elec Specialties RI | 8 | 8 | 14-Mar-14 | 25-Mar-14 | 57 |
| L06-6024 | L6 - Inspections | 2 | 2 | 28-Mar-14 | 31-Mar-14 | 30 |
| L06-6000 | L6 - Skim Ceiling | 4 | 4 | 04-Apr-14 | 09-Apr-14 | 37 |
| **Level 7 - (Guest Rooms)** | | | | | | |
| L07-6002 | L7 - Layout | 1 | 1 | 06-Mar-14 | 06-Mar-14 | 30 |
| L07-6004 | L7 - CMU Walls | 5 | 5 | 07-Mar-14 | 13-Mar-14 | 30 |
| L07-6008 | L7 - Int Wall Framing | 5 | 5 | 14-Mar-14 | 20-Mar-14 | 30 |
| L07-6010 | L7 - CMU Seismic Clips | 1 | 1 | 14-Mar-14 | 14-Mar-14 | 44 |
| L07-6012 | L7 - Fire Sprinkler RI | 10 | 10 | 21-Mar-14 | 03-Apr-14 | 30 |
| L07-6014 | L7 - Plumbing RI | 10 | 10 | 21-Mar-14 | 03-Apr-14 | 30 |
| L07-6016 | L7 - Electrical RI | 10 | 10 | 21-Mar-14 | 03-Apr-14 | 30 |

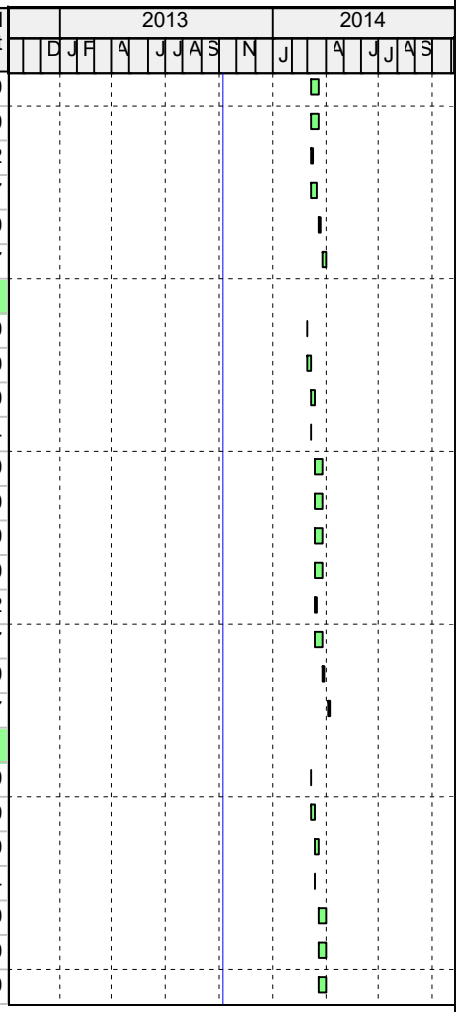



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6018 | L7 - HVAC RI | 10 | 10 | 21-Mar-14 | 03-Apr-14 | 30 |
| L07-6020 | L7 - H Mtl Frames | 3 | 3 | 21-Mar-14 | 25-Mar-14 | 42 |
| L07-6022 | L7 - Fire Alarm / Elec Specialties RI | 8 | 8 | 21-Mar-14 | 01-Apr-14 | 57 |
| L07-6024 | L7 - Inspections | 2 | 2 | 04-Apr-14 | 07-Apr-14 | 30 |
| L07-6000 | L7 - Skim Ceiling | 4 | 4 | 11-Apr-14 | 16-Apr-14 | 37 |
| **Level 8 - (Guest Rooms)** | | | | | | |
| L08-6002 | L8 - Layout | 1 | 1 | 13-Mar-14 | 13-Mar-14 | 30 |
| L08-6004 | L8 - CMU Walls | 5 | 5 | 14-Mar-14 | 20-Mar-14 | 30 |
| L08-6008 | L8 - Int Wall Framing | 5 | 5 | 21-Mar-14 | 27-Mar-14 | 30 |
| L08-6010 | L8 - CMU Seismic Clips | 1 | 1 | 21-Mar-14 | 21-Mar-14 | 44 |
| L08-6012 | L8 - Fire Sprinkler RI | 10 | 10 | 28-Mar-14 | 10-Apr-14 | 30 |
| L08-6014 | L8 - Plumbing RI | 10 | 10 | 28-Mar-14 | 10-Apr-14 | 30 |
| L08-6016 | L8 - Electrical RI | 10 | 10 | 28-Mar-14 | 10-Apr-14 | 30 |
| L08-6018 | L8 - HVAC RI | 10 | 10 | 28-Mar-14 | 10-Apr-14 | 30 |
| L08-6020 | L8 - H Mtl Frames | 3 | 3 | 28-Mar-14 | 01-Apr-14 | 42 |
| L08-6022 | L8 - Fire Alarm / Elec Specialties RI | 8 | 8 | 28-Mar-14 | 08-Apr-14 | 57 |
| L08-6024 | L8 - Inspections | 2 | 2 | 11-Apr-14 | 14-Apr-14 | 30 |
| L08-6000 | L8 - Skim Ceiling | 4 | 4 | 18-Apr-14 | 23-Apr-14 | 37 |
| **Level 9 - (Guest Rooms)** | | | | | | |
| L09-6002 | L9 - Layout | 1 | 1 | 20-Mar-14 | 20-Mar-14 | 30 |
| L09-6004 | L9 - CMU Walls | 5 | 5 | 21-Mar-14 | 27-Mar-14 | 30 |
| L09-6008 | L9 - Int Wall Framing | 5 | 5 | 28-Mar-14 | 03-Apr-14 | 30 |
| L09-6010 | L9 - CMU Seismic Clips | 1 | 1 | 28-Mar-14 | 28-Mar-14 | 44 |
| L09-6012 | L9 - Fire Sprinkler RI | 10 | 10 | 04-Apr-14 | 17-Apr-14 | 30 |
| L09-6014 | L9 - Plumbing RI | 10 | 10 | 04-Apr-14 | 17-Apr-14 | 30 |
| L09-6016 | L9 - Electrical RI | 10 | 10 | 04-Apr-14 | 17-Apr-14 | 30 |
| L09-6018 | L9 - HVAC RI | 10 | 10 | 04-Apr-14 | 17-Apr-14 | 30 |

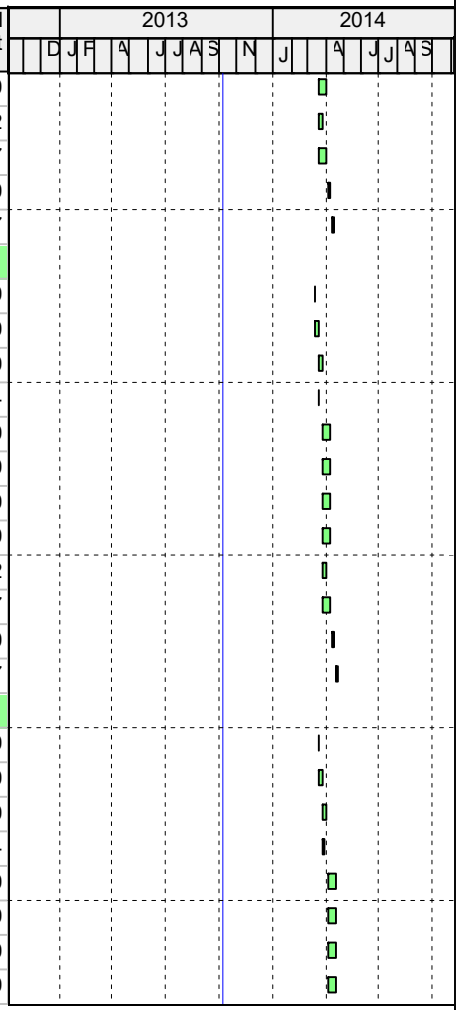



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6020 | L9 - H Mtl Frames | 3 | 3 | 04-Apr-14 | 08-Apr-14 | 42 |
| L09-6022 | L9 - Fire Alarm / Elec Specialties RI | 8 | 8 | 04-Apr-14 | 15-Apr-14 | 57 |
| L09-6024 | L9 - Inspections | 2 | 2 | 18-Apr-14 | 21-Apr-14 | 30 |
| L09-6000 | L9 - Skim Ceiling | 4 | 4 | 25-Apr-14 | 30-Apr-14 | 37 |
| **Level 10 - (Guest Rooms)** | | | | | | |
| L10-6002 | L10 - Layout | 1 | 1 | 27-Mar-14 | 27-Mar-14 | 30 |
| L10-6004 | L10 - CMU Walls | 5 | 5 | 28-Mar-14 | 03-Apr-14 | 30 |
| L10-6008 | L10 - Int Wall Framing | 5 | 5 | 04-Apr-14 | 10-Apr-14 | 30 |
| L10-6010 | L10 - CMU Seismic Clips | 1 | 1 | 04-Apr-14 | 04-Apr-14 | 44 |
| L10-6012 | L10 - Fire Sprinkler RI | 10 | 10 | 11-Apr-14 | 24-Apr-14 | 30 |
| L10-6014 | L10 - Plumbing RI | 10 | 10 | 11-Apr-14 | 24-Apr-14 | 30 |
| L10-6016 | L10 - Electrical RI | 10 | 10 | 11-Apr-14 | 24-Apr-14 | 30 |
| L10-6018 | L10 - HVAC RI | 10 | 10 | 11-Apr-14 | 24-Apr-14 | 30 |
| L10-6020 | L10 - H Mtl Frames | 3 | 3 | 11-Apr-14 | 15-Apr-14 | 42 |
| L10-6022 | L10 - Fire Alarm / Elec Specialties RI | 8 | 8 | 11-Apr-14 | 22-Apr-14 | 57 |
| L10-6024 | L10 - Inspections | 2 | 2 | 25-Apr-14 | 28-Apr-14 | 30 |
| L10-6000 | L10 - Skim Ceiling | 4 | 4 | 02-May-14 | 07-May-14 | 37 |
| **Level 11 - (Guest Rooms)** | | | | | | |
| L11-6002 | L11 - Layout | 1 | 1 | 03-Apr-14 | 03-Apr-14 | 49 |
| L11-6004 | L11 - CMU Walls | 5 | 5 | 04-Apr-14 | 10-Apr-14 | 49 |
| L11-6008 | L11 - Int Wall Framing | 5 | 5 | 11-Apr-14 | 17-Apr-14 | 49 |
| L11-6010 | L11 - CMU Seismic Clips | 1 | 1 | 11-Apr-14 | 11-Apr-14 | 63 |
| L11-6012 | L11 - Fire Sprinkler RI | 10 | 10 | 18-Apr-14 | 01-May-14 | 49 |
| L11-6014 | L11 - Plumbing RI | 10 | 10 | 18-Apr-14 | 01-May-14 | 49 |
| L11-6016 | L11 - Electrical RI | 10 | 10 | 18-Apr-14 | 01-May-14 | 49 |
| L11-6018 | L11 - HVAC RI | 10 | 10 | 18-Apr-14 | 01-May-14 | 49 |
| L11-6020 | L11 - H Mtl Frames | 3 | 3 | 18-Apr-14 | 22-Apr-14 | 61 |

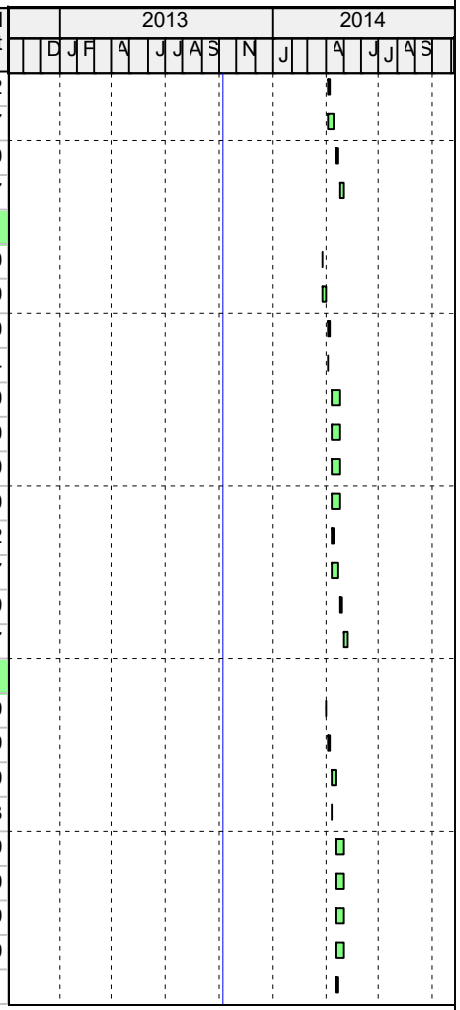



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6022 | L11 - Fire Alarm / Elec Specialties Rl | 8 | 8 | 18-Apr-14 | 29-Apr-14 | 76 |
| L11-6024 | L11 - Inspections | 2 | 2 | 02-May-14 | 05-May-14 | 49 |
| L11-6000 | L11 - Skim Ceiling | 4 | 4 | 09-May-14 | 14-May-14 | 56 |
| **Level 12 - (Guest Rooms)** | | | | | | |
| L12-6002 | L12 - Layout | 1 | 1 | 17-Apr-14 | 17-Apr-14 | 44 |
| L12-6004 | L12 - CMU Walls | 5 | 5 | 18-Apr-14 | 24-Apr-14 | 44 |
| L12-6008 | L12 - Int Wall Framing | 5 | 5 | 25-Apr-14 | 01-May-14 | 44 |
| L12-6010 | L12 - CMU Seismic Clips | 1 | 1 | 25-Apr-14 | 25-Apr-14 | 58 |
| L12-6012 | L12 - Fire Sprinkler Rl | 10 | 10 | 02-May-14 | 15-May-14 | 44 |
| L12-6014 | L12 - Plumbing Rl | 10 | 10 | 02-May-14 | 15-May-14 | 44 |
| L12-6016 | L12 - Electrical Rl | 10 | 10 | 02-May-14 | 15-May-14 | 44 |
| L12-6018 | L12 - HVAC Rl | 10 | 10 | 02-May-14 | 15-May-14 | 44 |
| L12-6020 | L12 - H Mtl Frames | 3 | 3 | 02-May-14 | 06-May-14 | 56 |
| L12-6022 | L12 - Fire Alarm / Elec Specialties Rl | 8 | 8 | 02-May-14 | 13-May-14 | 71 |
| L12-6024 | L12 - Inspections | 2 | 2 | 16-May-14 | 19-May-14 | 44 |
| L12-6000 | L12 - Skim Ceiling | 4 | 4 | 23-May-14 | 29-May-14 | 51 |
| **Level 14 - (Guest Rooms)** | | | | | | |
| L14-6002 | L14 - Layout | 1 | 1 | 21-Apr-14 | 21-Apr-14 | 47 |
| L14-6004 | L14 - CMU Walls | 5 | 5 | 22-Apr-14 | 28-Apr-14 | 47 |
| L14-6008 | L14 - Int Wall Framing | 5 | 5 | 29-Apr-14 | 05-May-14 | 47 |
| L14-6010 | L14 - CMU Seismic Clips | 1 | 1 | 29-Apr-14 | 29-Apr-14 | 61 |
| L14-6012 | L14 - Fire Sprinkler Rl | 10 | 10 | 06-May-14 | 19-May-14 | 47 |
| L14-6014 | L14 - Plumbing Rl | 10 | 10 | 06-May-14 | 19-May-14 | 47 |
| L14-6016 | L14 - Electrical Rl | 10 | 10 | 06-May-14 | 19-May-14 | 47 |
| L14-6018 | L14 - HVAC Rl | 10 | 10 | 06-May-14 | 19-May-14 | 47 |
| L14-6020 | L14 - H Mtl Frames | 3 | 3 | 06-May-14 | 08-May-14 | 59 |
| L14-6022 | L14 - Fire Alarm / Elec Specialties Rl | 8 | 8 | 06-May-14 | 15-May-14 | 74 |

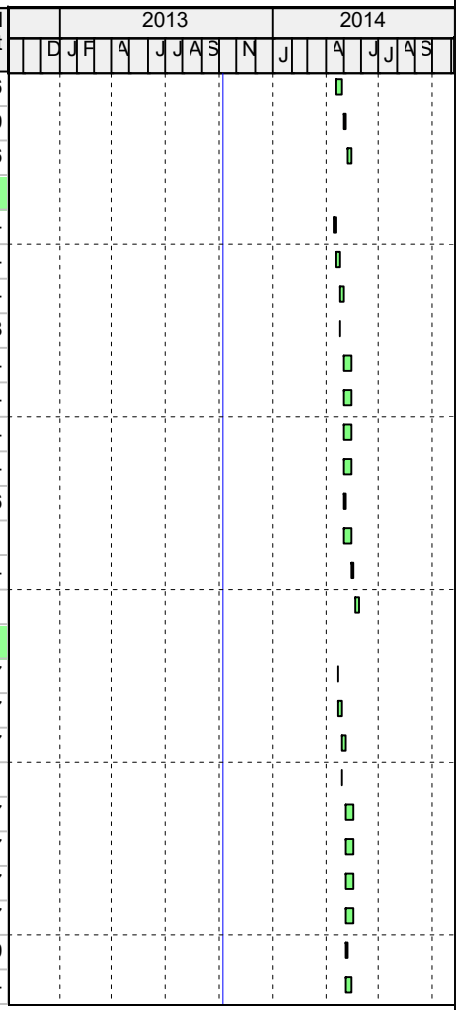



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6024 | L14 - Inspections | 2 | 2 | 20-May-14 | 21-May-14 | 47 |
| L14-6000 | L14 - Skim Ceiling | 4 | 4 | 28-May-14 | 02-Jun-14 | 54 |
| **Level 15 - (Guest Rooms)** | | | | | | |
| L15-6002 | L15 - Layout | 1 | 1 | 23-Apr-14 | 23-Apr-14 | 50 |
| L15-6004 | L15 - CMU Walls | 5 | 5 | 24-Apr-14 | 30-Apr-14 | 50 |
| L15-6008 | L15 - Int Wall Framing | 5 | 5 | 01-May-14 | 07-May-14 | 50 |
| L15-6010 | L15 - CMU Seismic Clips | 1 | 1 | 01-May-14 | 01-May-14 | 64 |
| L15-6012 | L15 - Fire Sprinkler RI | 10 | 10 | 08-May-14 | 21-May-14 | 50 |
| L15-6014 | L15 - Plumbing RI | 10 | 10 | 08-May-14 | 21-May-14 | 50 |
| L15-6016 | L15 - Electrical RI | 10 | 10 | 08-May-14 | 21-May-14 | 50 |
| L15-6018 | L15 - HVAC RI | 10 | 10 | 08-May-14 | 21-May-14 | 50 |
| L15-6020 | L15 - H Mtl Frames | 3 | 3 | 08-May-14 | 12-May-14 | 62 |
| L15-6022 | L15 - Fire Alarm / Elec Specialties RI | 8 | 8 | 08-May-14 | 19-May-14 | 77 |
| L15-6024 | L15 - Inspections | 2 | 2 | 22-May-14 | 23-May-14 | 50 |
| L15-6000 | L15 - Skim Ceiling | 4 | 4 | 30-May-14 | 04-Jun-14 | 57 |
| **Level 16 - (Guest Rooms)** | | | | | | |
| L16-6002 | L16 - Layout | 1 | 1 | 25-Apr-14 | 25-Apr-14 | 53 |
| L16-6004 | L16 - CMU Walls | 5 | 5 | 28-Apr-14 | 02-May-14 | 53 |
| L16-6008 | L16 - Int Wall Framing | 5 | 5 | 05-May-14 | 09-May-14 | 53 |
| L16-6010 | L16 - CMU Seismic Clips | 1 | 1 | 05-May-14 | 05-May-14 | 67 |
| L16-6012 | L16 - Fire Sprinkler RI | 10 | 10 | 12-May-14 | 23-May-14 | 53 |
| L16-6014 | L16 - Plumbing RI | 10 | 10 | 12-May-14 | 23-May-14 | 53 |
| L16-6016 | L16 - Electrical RI | 10 | 10 | 12-May-14 | 23-May-14 | 53 |
| L16-6018 | L16 - HVAC RI | 10 | 10 | 12-May-14 | 23-May-14 | 53 |
| L16-6020 | L16 - H Mtl Frames | 3 | 3 | 12-May-14 | 14-May-14 | 65 |
| L16-6022 | L16 - Fire Alarm / Elec Specialties RI | 8 | 8 | 12-May-14 | 21-May-14 | 80 |
| L16-6024 | L16 - Inspections | 2 | 2 | 27-May-14 | 28-May-14 | 53 |

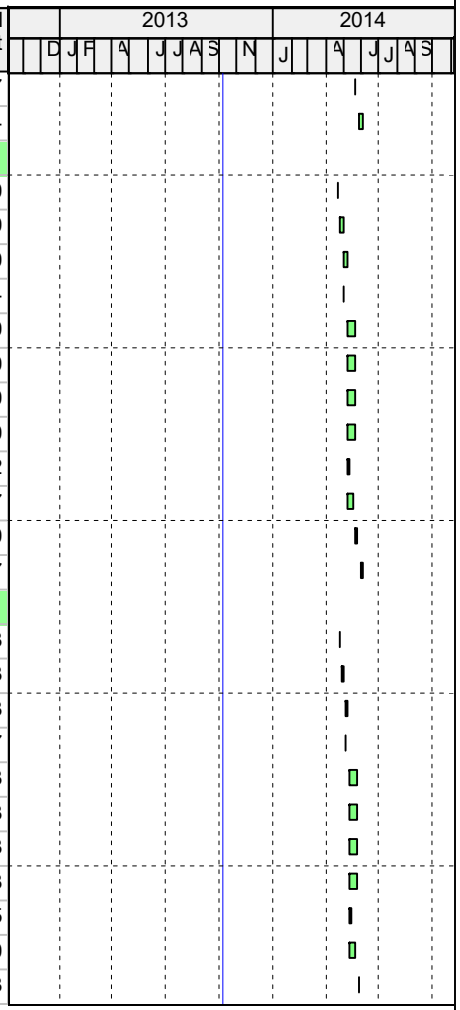



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6000 | L16 - Skim Ceiling | 4 | 4 | 03-Jun-14 | 06-Jun-14 | 60 |
| **Level 17 - (Guest Rooms)** | | | | | | |
| L17-6002 | L17 - Layout | 1 | 1 | 29-Apr-14 | 29-Apr-14 | 56 |
| L17-6004 | L17 - CMU Walls | 5 | 5 | 30-Apr-14 | 06-May-14 | 56 |
| L17-6008 | L17 - Int Wall Framing | 5 | 5 | 07-May-14 | 13-May-14 | 56 |
| L17-6010 | L17 - CMU Seismic Clips | 1 | 1 | 07-May-14 | 07-May-14 | 70 |
| L17-6012 | L17 - Fire Sprinkler Rl | 10 | 10 | 14-May-14 | 28-May-14 | 56 |
| L17-6014 | L17 - Plumbing Rl | 10 | 10 | 14-May-14 | 28-May-14 | 56 |
| L17-6016 | L17 - Electrical Rl | 10 | 10 | 14-May-14 | 28-May-14 | 56 |
| L17-6018 | L17 - HVAC Rl | 10 | 10 | 14-May-14 | 28-May-14 | 56 |
| L17-6020 | L17 - H Mtl Frames | 3 | 3 | 14-May-14 | 16-May-14 | 68 |
| L17-6022 | L17 - Fire Alarm / Elec Specialties Rl | 8 | 8 | 14-May-14 | 23-May-14 | 83 |
| L17-6024 | L17 - Inspections | 2 | 2 | 29-May-14 | 30-May-14 | 56 |
| L17-6000 | L17 - Skim Ceiling | 4 | 4 | 05-Jun-14 | 10-Jun-14 | 63 |
| **Mechanical Penthouse** | | | | | | |
| PH-6002 | PH - Layout | 1 | 1 | 30-Apr-14 | 30-Apr-14 | 58 |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 5 | 01-May-14 | 07-May-14 | 69 |
| PH-6006 | PH - Ext Wall Framing - (Incldg Roof Parapet) | 10 | 10 | 01-May-14 | 14-May-14 | 58 |
| PH-6008 | PH - Int Wall Framing | 3 | 3 | 15-May-14 | 19-May-14 | 58 |
| PH-6012 | PH - Fire Sprinkler Rl | 8 | 8 | 20-May-14 | 30-May-14 | 65 |
| PH-6014 | PH - Plumbing Rl | 12 | 12 | 20-May-14 | 05-Jun-14 | 61 |
| PH-6016 | PH - Electrical Rl | 12 | 12 | 20-May-14 | 05-Jun-14 | 61 |
| PH-6018 | PH - HVAC Rl | 15 | 15 | 20-May-14 | 10-Jun-14 | 58 |
| PH-6020 | PH - H Mtl Frames | 2 | 2 | 20-May-14 | 21-May-14 | 76 |
| PH-6022 | PH - Fire Alarm / Elec Specialties Rl | 5 | 5 | 20-May-14 | 27-May-14 | 89 |
| PH-6024 | PH - Inspections | 2 | 2 | 11-Jun-14 | 12-Jun-14 | 58 |
| **Finishes** | | | | | | |

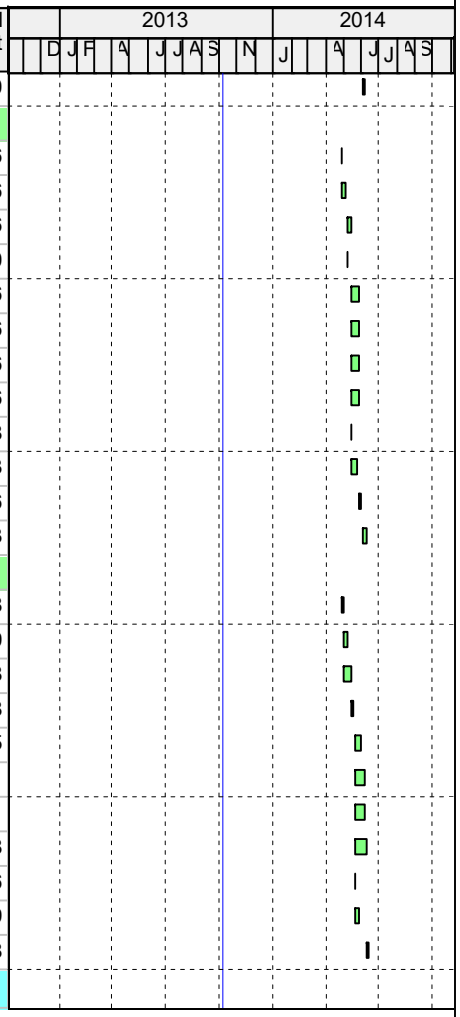



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL4-8100 | LL4 - Insulation | 1 | 1 | 14-Feb-14 | 14-Feb-14 | 70 |
| LL4-8102 | LL4 - GWB Hang / Tape / Finish - (Including Commor | 5 | 5 | 17-Feb-14 | 21-Feb-14 | 70 |
| LL4-8104 | LL4 - Int Painting | 3 | 3 | 19-Feb-14 | 21-Feb-14 | 93 |
| LL4-8110 | LL4 - HVAC Trim / Finish | 6 | 6 | 24-Feb-14 | 03-Mar-14 | 94 |
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 5 | 5 | 24-Feb-14 | 28-Feb-14 | 95 |
| LL4-8114 | LL4 - Striping / Signage | 3 | 3 | 24-Feb-14 | 26-Feb-14 | 106 |
| LL4-8118 | LL4 - Elec Specialties Trim / Finish | 4 | 4 | 24-Feb-14 | 27-Feb-14 | 96 |
| LL4-8122 | LL4 - Plumbing Trim / Finish | 5 | 5 | 04-Mar-14 | 10-Mar-14 | 93 |
| LL4-8108 | LL4 - Elec Trim / Finish | 6 | 6 | 07-Mar-14 | 14-Mar-14 | 85 |
| LL4-6026 | LL4 - Pull Wire | 6 | 6 | 07-Mar-14 | 14-Mar-14 | 85 |
| LL4-8124 | LL4 - Flooring | 3 | 3 | 17-Mar-14 | 19-Mar-14 | 85 |
| LL4-8126 | LL4 - Doors & Hardware | 3 | 3 | 18-Mar-14 | 20-Mar-14 | 85 |
| LL4-8130 | LL4 - Substantially Complete | 0 | 0 | | 20-Mar-14 | 85 |
| LL4-8132 | LL4 - Contractor Pre-Punchlist | 5 | 5 | 21-Mar-14 | 27-Mar-14 | 88 |
| LL4-8134 | LL4 - Pre-Clean | 5 | 5 | 21-Mar-14 | 27-Mar-14 | 85 |
| LL4-8208 | LL4 - Final Clean | 3 | 3 | 28-Mar-14 | 01-Apr-14 | 85 |
| LL4-8210 | LL4 - Owner Walk / Create Punchlist | 1 | 1 | 02-Apr-14 | 02-Apr-14 | 85 |
| LL4-8212 | LL4 - Final Punchlist | 5 | 5 | 03-Apr-14 | 09-Apr-14 | 85 |
| LL4-8214 | LL4 - Floor Complete | 0 | 0 | | 09-Apr-14 | 85 |
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL3-8100 | LL3 - Insulation | 1 | 1 | 07-Mar-14 | 07-Mar-14 | 56 |
| LL3-8102 | LL3 - GWB Hang / Tape / Finish - (Including Commor | 5 | 5 | 10-Mar-14 | 14-Mar-14 | 58 |
| LL3-6026 | LL3 - Pull Wire | 6 | 6 | 10-Mar-14 | 17-Mar-14 | 89 |

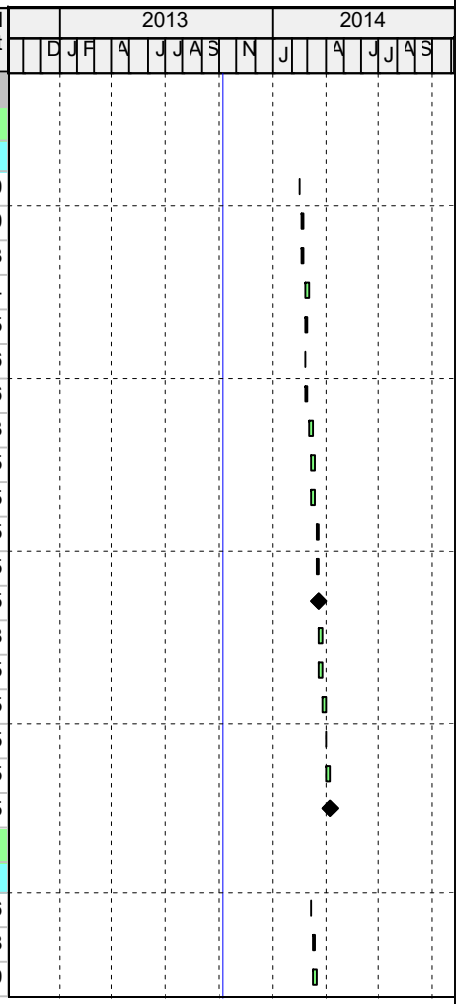



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-8104 | LL3 - Int Painting | 3 | 3 | 12-Mar-14 | 14-Mar-14 | 83 |
| LL3-8108 | LL3 - Elec Trim / Finish | 6 | 6 | 17-Mar-14 | 24-Mar-14 | 84 |
| LL3-8110 | LL3 - HVAC Trim / Finish | 6 | 6 | 17-Mar-14 | 24-Mar-14 | 84 |
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 5 | 5 | 17-Mar-14 | 21-Mar-14 | 85 |
| LL3-8114 | LL3 - Striping / Signage | 3 | 3 | 17-Mar-14 | 19-Mar-14 | 96 |
| LL3-8118 | LL3 - Elec Specialties Trim / Finish | 4 | 4 | 17-Mar-14 | 20-Mar-14 | 86 |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 5 | 5 | 25-Mar-14 | 31-Mar-14 | 83 |
| LL3-8124 | LL3 - Flooring | 3 | 3 | 25-Mar-14 | 27-Mar-14 | 84 |
| LL3-8126 | LL3 - Doors & Hardware | 3 | 3 | 26-Mar-14 | 28-Mar-14 | 84 |
| LL3-8130 | LL3 - Substantially Complete | 0 | 0 | | 31-Mar-14 | 83 |
| LL3-8132 | LL3 - Contractor Pre-Punchlist | 5 | 5 | 01-Apr-14 | 07-Apr-14 | 86 |
| LL3-8134 | LL3 - Pre-Clean | 5 | 5 | 01-Apr-14 | 07-Apr-14 | 83 |
| LL3-8208 | LL3 - Final Clean | 3 | 3 | 08-Apr-14 | 10-Apr-14 | 83 |
| LL3-8210 | LL3 - Owner Walk / Create Punchlist | 1 | 1 | 11-Apr-14 | 11-Apr-14 | 83 |
| LL3-8212 | LL3 - Final Punchlist | 5 | 5 | 14-Apr-14 | 18-Apr-14 | 83 |
| LL3-8214 | LL3 - Floor Complete | 0 | 0 | | 18-Apr-14 | 83 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL2-8100 | LL2 - Insulation | 5 | 5 | 18-Jun-14 | 24-Jun-14 | -15 |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish - (Including Commor | 15 | 15 | 25-Jun-14 | 16-Jul-14 | -15 |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 10 | 10 | 25-Jun-14 | 09-Jul-14 | 13 |
| LL2-6026 | LL2 - Pull Wire | 15 | 15 | 25-Jun-14 | 16-Jul-14 | 7 |
| LL2-8128 | LL2 - Entry Gates | 3 | 3 | 10-Jul-14 | 14-Jul-14 | 13 |
| LL2-8104 | LL2 - Int Painting | 5 | 5 | 14-Jul-14 | 18-Jul-14 | -15 |
| LL2-8136 | LL2 - Chainlink Fencing / Gate @ Recycling | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 13 |
| LL2-8120 | LL2 - Steel Pipe Guardrails | 6 | 6 | 17-Jul-14 | 24-Jul-14 | 7 |
| LL2-8108 | LL2 - Elec Trim / Finish | 20 | 20 | 21-Jul-14 | 15-Aug-14 | -15 |

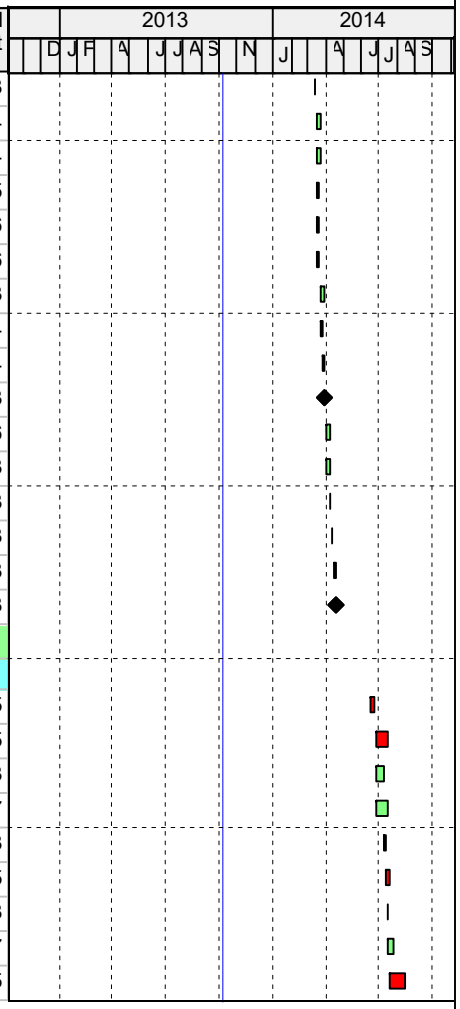



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-8110 | LL2 - HVAC Trim / Finish | 12 | 12 | 21-Jul-14 | 05-Aug-14 | -7 |
| LL2-8112 | LL2 - Fire Sprinkler Trim / Finish | 8 | 8 | 21-Jul-14 | 30-Jul-14 | -3 |
| LL2-8114 | LL2 - Striping / Signage | 3 | 3 | 21-Jul-14 | 23-Jul-14 | 13 |
| LL2-8116 | LL2 - Finish Carpentry / Millwork | 2 | 2 | 21-Jul-14 | 22-Jul-14 | 2 |
| LL2-8118 | LL2 - Elec Specialties Trim / Finish | 4 | 4 | 21-Jul-14 | 24-Jul-14 | 1 |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 9 | 9 | 21-Jul-14 | 31-Jul-14 | 2 |
| LL2-8122 | LL2 - Plumbing Trim / Finish | 5 | 5 | 25-Jul-14 | 31-Jul-14 | 2 |
| LL2-8126 | LL2 - Doors & Hardware | 7 | 7 | 15-Aug-14 | 25-Aug-14 | -15 |
| LL2-8124 | LL2 - Flooring | 5 | 5 | 18-Aug-14 | 22-Aug-14 | -15 |
| LL2-8130 | LL2 - Substantially Complete | 0 | 0 | | 25-Aug-14 | -15 |
| LL2-8132 | LL2 - Contractor Pre-Punchlist | 5 | 5 | 26-Aug-14 | 02-Sep-14 | -12 |
| LL2-8134 | LL2 - Pre-Clean | 5 | 5 | 26-Aug-14 | 02-Sep-14 | -15 |
| LL2-8208 | LL2 - Final Clean | 3 | 3 | 03-Sep-14 | 05-Sep-14 | -15 |
| LL2-8210 | LL2 - Owner Walk / Create Punchlist | 1 | 1 | 08-Sep-14 | 08-Sep-14 | -15 |
| LL2-8212 | LL2 - Final Punchlist | 5 | 5 | 09-Sep-14 | 15-Sep-14 | -15 |
| LL2-8214 | LL2 - Floor Complete | 0 | 0 | | 15-Sep-14 | -15 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1-8100 | LL1 - Insulation | 5 | 5 | 04-Apr-14 | 10-Apr-14 | -18 |
| LL1-8102 | LL1 - GWB Hang / Tape / Finish - (Including Commor | 20 | 20 | 11-Apr-14 | 08-May-14 | -18 |
| LL1-6026 | LL1 - Pull Wire | 10 | 10 | 11-Apr-14 | 24-Apr-14 | 19 |
| LL1-8104 | LL1 - Int Painting | 10 | 10 | 06-May-14 | 19-May-14 | -18 |
| LL1-8106 | LL1 - Wallcoverings | 6 | 6 | 08-May-14 | 15-May-14 | 4 |
| LL1-8116 | LL1 - Finish Carpentry / Millwork | 10 | 10 | 13-May-14 | 27-May-14 | -7 |
| LL1-8120 | LL1 - Ceramic Tile / Counter Tops | 12 | 12 | 15-May-14 | 02-Jun-14 | -7 |
| LL1-8122 | LL1 - Plumbing Trim / Finish | 10 | 10 | 19-May-14 | 02-Jun-14 | -1 |
| LL1-8112 | LL1 - Fire Sprinkler Trim / Finish | 8 | 8 | 20-May-14 | 30-May-14 | -6 |

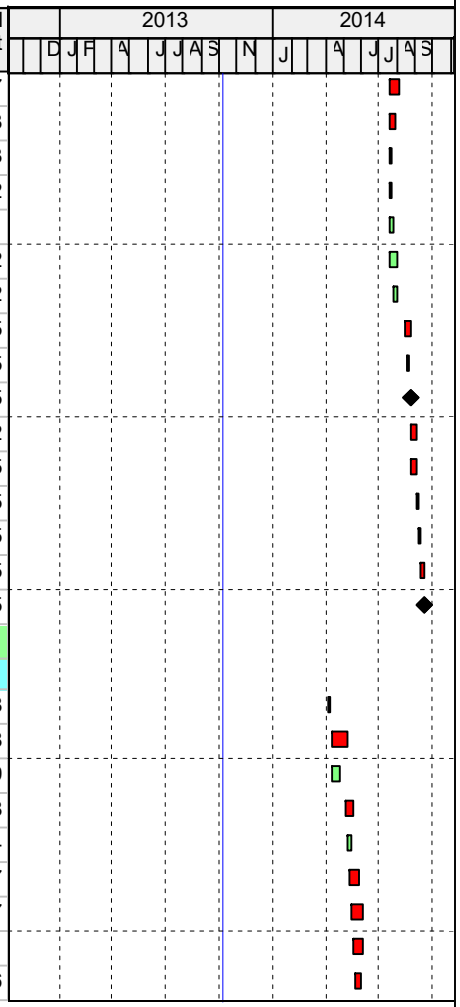



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-8118 | LL1 - Elec Specialties Trim / Finish | 6 | 6 | 20-May-14 | 28-May-14 | -4 |
| LL1-8114 | LL1 - T-Bar Grid Ceiling | 8 | 8 | 20-May-14 | 30-May-14 | -18 |
| LL1-8138 | LL1 - Epoxy Flooring @ Food Prep | 7 | 7 | 28-May-14 | 05-Jun-14 | -1 |
| LL1-8142 | LL1 - Folding Partitions @ Meeting Rooms | 8 | 8 | 28-May-14 | 06-Jun-14 | -2 |
| LL1-8108 | LL1 - Elec Trim / Finish | 12 | 12 | 02-Jun-14 | 17-Jun-14 | -18 |
| LL1-8110 | LL1 - HVAC Trim / Finish | 10 | 10 | 02-Jun-14 | 13-Jun-14 | -16 |
| LL1-8128 | LL1 - Bath Specialties | 3 | 3 | 03-Jun-14 | 05-Jun-14 | -1 |
| LL1-8136 | LL1 - Toilet Partitions | 3 | 3 | 03-Jun-14 | 05-Jun-14 | -1 |
| LL1-8124 | LL1 - Flooring @ Meeting Rooms | 8 | 8 | 18-Jun-14 | 27-Jun-14 | -18 |
| LL1-8140 | LL1 - Acoustical Ceiling Tile | 5 | 5 | 18-Jun-14 | 24-Jun-14 | -14 |
| LL1-8126 | LL1 - Doors & Hardware | 8 | 8 | 19-Jun-14 | 30-Jun-14 | -18 |
| LL1-8130 | LL1 - Meeting Rooms / Food Prep Substantially Com | 0 | 0 | | 30-Jun-14 | -18 |
| LL1-8132 | LL1 - Contractor Pre-Punchlist | 10 | 10 | 01-Jul-14 | 15-Jul-14 | 31 |
| LL1-8134 | LL1 - Pre-Clean | 8 | 8 | 01-Jul-14 | 11-Jul-14 | 28 |
| **Corridors / Common / Public Areas** | | | | | | |
| LL1-8200 | LL1 - Final Paint @ Common / Public Areas | 6 | 6 | 01-Jul-14 | 09-Jul-14 | -18 |
| LL1-8202 | LL1 - Elec Trim / Finish @ Common / Public Areas | 10 | 10 | 10-Jul-14 | 23-Jul-14 | -18 |
| LL1-8204 | LL1 - Mech Trim / Finish @ Common / Public Areas | 8 | 8 | 10-Jul-14 | 21-Jul-14 | -16 |
| LL1-8206 | LL1 - Flooring @ Common / Public Areas | 6 | 6 | 23-Jul-14 | 30-Jul-14 | 15 |
| LL1-8208 | LL1 - Final Clean | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 15 |
| LL1-8210 | LL1 - Owner Walk / Create Punchlist | 1 | 1 | 07-Aug-14 | 07-Aug-14 | 15 |
| LL1-8212 | LL1 - Final Punchlist | 10 | 10 | 16-Sep-14 | 29-Sep-14 | -11 |
| LL1-8214 | LL1 - Floor Complete | 0 | 0 | | 29-Sep-14 | -11 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| L01-8200 | L1 - Final Paint @ Common / Public Areas | 6 | 6 | 15-Jul-14 | 22-Jul-14 | -25 |
| L01-8202 | L1 - Elec Trim / Finish @ Common / Public Areas | 8 | 8 | 23-Jul-14 | 01-Aug-14 | -25 |

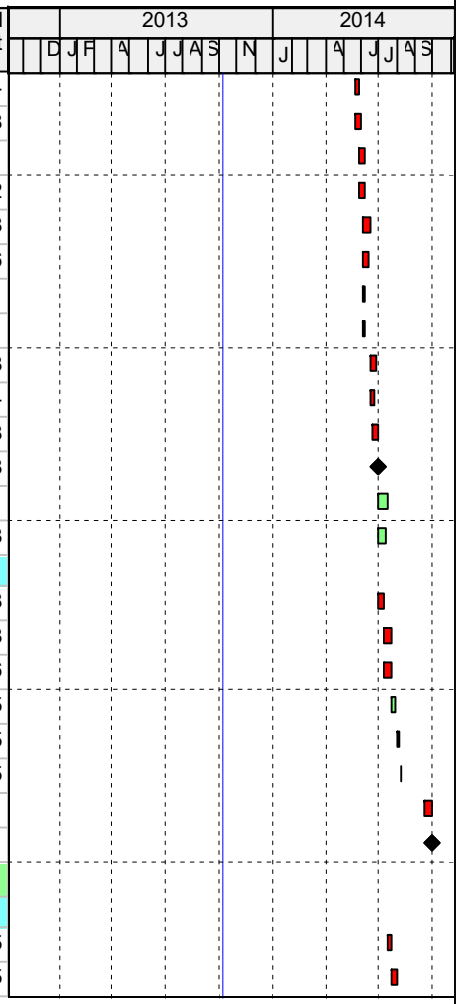



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L01-8204 | L1 - Mech Trim / Finish @ Common / Public Areas | 8 | 8 | 23-Jul-14 | 01-Aug-14 | -25 |
| L01-8206 | L1 - Flooring @ Common / Public Areas | 10 | 10 | 01-Aug-14 | 14-Aug-14 | -10 |
| L01-8208 | L1 - Final Clean | 5 | 5 | 15-Aug-14 | 21-Aug-14 | -10 |
| L01-8216 | L1 - Entry Mats | 2 | 2 | 15-Aug-14 | 18-Aug-14 | -7 |
| L01-8210 | L1 - Owner Walk / Create Punchlist | 1 | 1 | 22-Aug-14 | 22-Aug-14 | -10 |
| L01-8212 | L1 - Final Punchlist | 10 | 10 | 25-Aug-14 | 08-Sep-14 | -10 |
| L01-8214 | L1 - Floor Complete | 0 | 0 | | 08-Sep-14 | -10 |
| **Main Ballrooms / Meeting Rooms / Kitchen / Lobby / Dining** | | | | | | |
| L01-8100 | L1 - Insulation | 5 | 5 | 29-Apr-14 | 05-May-14 | -25 |
| L01-6026 | L1 - Pull Wire | 10 | 10 | 29-Apr-14 | 12-May-14 | 9 |
| L01-8102 | L1 - GWB Hang / Tape / Finish - (Including Common / | 20 | 20 | 06-May-14 | 03-Jun-14 | -25 |
| L01-8104 | L1 - Int Painting | 10 | 10 | 30-May-14 | 12-Jun-14 | -25 |
| L01-8106 | L1 - Wallcoverings | 6 | 6 | 03-Jun-14 | 10-Jun-14 | -11 |
| L01-8116 | L1 - Finish Carpentry / Millwork | 14 | 14 | 06-Jun-14 | 25-Jun-14 | -22 |
| L01-8120 | L1 - Ceramic Tile / Counter Tops @ Restrooms | 12 | 12 | 10-Jun-14 | 25-Jun-14 | -22 |
| L01-8122 | L1 - Plumbing Trim / Finish | 10 | 10 | 12-Jun-14 | 25-Jun-14 | -16 |
| L01-8108 | L1 - Elec Trim / Finish | 12 | 12 | 13-Jun-14 | 30-Jun-14 | -25 |
| L01-8110 | L1 - HVAC Trim / Finish | 10 | 10 | 13-Jun-14 | 26-Jun-14 | -23 |
| L01-8112 | L1 - Fire Sprinkler Trim / Finish | 8 | 8 | 13-Jun-14 | 24-Jun-14 | -21 |
| L01-8118 | L1 - Elec Specialties Trim / Finish | 6 | 6 | 13-Jun-14 | 20-Jun-14 | -19 |
| L01-8136 | L1 - Casework / Front Desk | 10 | 10 | 13-Jun-14 | 26-Jun-14 | -14 |
| L01-8140 | L1 - Tile Flooring @ Kitchen | 12 | 12 | 13-Jun-14 | 30-Jun-14 | -16 |
| L01-8142 | L1 - Folding Partitions @ Ballrooms | 10 | 10 | 13-Jun-14 | 26-Jun-14 | -14 |
| L01-8128 | L1 - Bath Specialties | 3 | 3 | 26-Jun-14 | 30-Jun-14 | -16 |
| L01-8138 | L1 - Toilet Partitions | 3 | 3 | 26-Jun-14 | 30-Jun-14 | -16 |
| L01-8124 | L1 - Flooring @ Ballrooms | 8 | 8 | 01-Jul-14 | 11-Jul-14 | -25 |
| L01-8126 | L1 - Doors & Hardware | 8 | 8 | 02-Jul-14 | 14-Jul-14 | -25 |

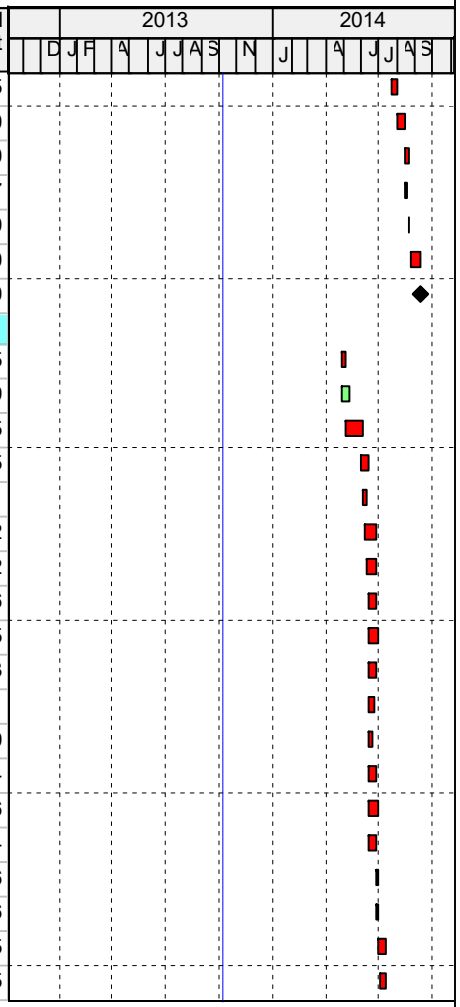



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L01-8130 | L1 - Ballrooms / Kitchen / Restrooms Substantially Cc | 0 | 0 | | 14-Jul-14 | -25 |
| L01-8132 | L1 - Contractor Pre-Punchlist | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 13 |
| L01-8134 | L1 - Pre-Clean | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 8 |
| L01-8114 | L1 - Signage | 3 | 3 | 23-Jul-14 | 25-Jul-14 | 4 |
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8100 | L2 - Insulation | 5 | 5 | 17-Apr-14 | 23-Apr-14 | -2 |
| L02-6026 | L2 - Pull Wire | 6 | 6 | 17-Apr-14 | 24-Apr-14 | 21 |
| L02-8102 | L2 - GWB Hang / Tape / Finish - (Including Common / | 16 | 16 | 20-May-14 | 11-Jun-14 | -20 |
| L02-8104 | L2 - Int Painting | 8 | 8 | 09-Jun-14 | 18-Jun-14 | -20 |
| L02-8106 | L2 - Wallcoverings | 6 | 6 | 11-Jun-14 | 18-Jun-14 | -10 |
| L02-8116 | L2 - Finish Carpentry / Millwork | 5 | 5 | 16-Jun-14 | 20-Jun-14 | -17 |
| L02-8120 | L2 - Ceramic Tile / Counter Tops | 8 | 8 | 18-Jun-14 | 27-Jun-14 | -17 |
| L02-8108 | L2 - Elec Trim / Finish | 10 | 10 | 19-Jun-14 | 02-Jul-14 | -20 |
| L02-8110 | L2 - HVAC Trim / Finish | 10 | 10 | 19-Jun-14 | 02-Jul-14 | -20 |
| L02-8112 | L2 - Fire Sprinkler Trim / Finish | 8 | 8 | 19-Jun-14 | 30-Jun-14 | -18 |
| L02-8118 | L2 - Elec Specialties Trim / Finish | 6 | 6 | 19-Jun-14 | 26-Jun-14 | -16 |
| L02-8136 | L2 - Lockers / Benches @ Locker Rooms | 5 | 5 | 19-Jun-14 | 25-Jun-14 | -9 |
| L02-8122 | L2 - Plumbing Trim / Finish | 8 | 8 | 20-Jun-14 | 01-Jul-14 | -15 |
| L02-8128 | L2 - Bath Specialties | 2 | 2 | 02-Jul-14 | 03-Jul-14 | -15 |
| L02-8124 | L2 - Flooring | 5 | 5 | 03-Jul-14 | 10-Jul-14 | -20 |
| L02-8126 | L2 - Doors & Hardware | 5 | 5 | 07-Jul-14 | 11-Jul-14 | -20 |
| L02-8130 | L2 - Admin / Employee Rooms Substantially Complet | 0 | 0 | | 11-Jul-14 | -20 |
| L02-8132 | L2 - Contractor Pre-Punchlist | 5 | 5 | 14-Jul-14 | 18-Jul-14 | 19 |
| L02-8134 | L2 - Pre-Clean | 5 | 5 | 14-Jul-14 | 18-Jul-14 | 16 |
| **Corridors** | | | | | | |
| L02-8200 | L2 - Final Paint @ Common / Public Areas | 5 | 5 | 14-Jul-14 | 18-Jul-14 | -20 |

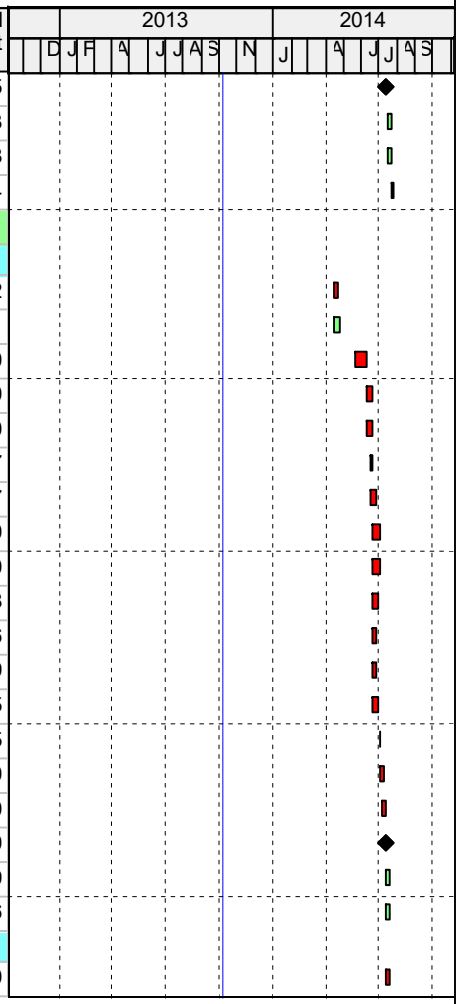



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8114 | L2 - Signage | 3 | 3 | 21-Jul-14 | 23-Jul-14 | 13 |
| L02-8202 | L2 - Elec Trim / Finish @ Common / Public Areas | 5 | 5 | 21-Jul-14 | 25-Jul-14 | -20 |
| L02-8204 | L2 - Mech Trim / Finish @ Common / Public Areas | 5 | 5 | 21-Jul-14 | 25-Jul-14 | -20 |
| L02-8206 | L2 - Flooring @ Corridors | 3 | 3 | 28-Jul-14 | 30-Jul-14 | 8 |
| L02-8208 | L2 - Final Clean | 3 | 3 | 31-Jul-14 | 04-Aug-14 | 8 |
| L02-8210 | L2 - Owner Walk / Create Punchlist | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 8 |
| L02-8212 | L2 - Final Punchlist | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 8 |
| L02-8214 | L2 - Floor Complete | 0 | 0 | | 12-Aug-14 | 8 |
| Upper Tower - (Levels 3 thru PH) | | | | | | |
| Level 3 - (Guest Rooms / Pool) | | | | | | |
| Guest Rooms | | | | | | |
| L03-8100 | L3 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 11-Mar-14 | 13-Mar-14 | 30 |
| L03-6026 | L3 - Pull Wire | 6 | 6 | 11-Mar-14 | 18-Mar-14 | 53 |
| L03-8102 | L3 - GWB Hang / Tape / Finish - (Including Common / | 14 | 14 | 14-Mar-14 | 02-Apr-14 | 30 |
| L03-8104 | L3 - Int Painting | 5 | 5 | 31-Mar-14 | 04-Apr-14 | 30 |
| L03-8106 | L3 - Wallcoverings | 6 | 6 | 02-Apr-14 | 09-Apr-14 | 37 |
| L03-8108 | L3 - Elec Trim / Finish | 8 | 8 | 07-Apr-14 | 16-Apr-14 | 32 |
| L03-8110 | L3 - HVAC Trim / Finish | 8 | 8 | 07-Apr-14 | 16-Apr-14 | 32 |
| L03-8112 | L3 - Fire Sprinkler Trim / Finish | 8 | 8 | 07-Apr-14 | 16-Apr-14 | 32 |
| L03-8116 | L3 - Finish Carpentry / Millwork | 8 | 8 | 07-Apr-14 | 16-Apr-14 | 30 |
| L03-8118 | L3 - Elec Specialties Trim / Finish | 4 | 4 | 07-Apr-14 | 10-Apr-14 | 36 |
| L03-8120 | L3 - Ceramic Tile / Counter Tops | 8 | 8 | 09-Apr-14 | 18-Apr-14 | 30 |
| L03-8122 | L3 - Plumbing Trim / Finish | 8 | 8 | 11-Apr-14 | 22-Apr-14 | 31 |
| L03-8126 | L3 - Doors & Hardware | 8 | 8 | 17-Apr-14 | 28-Apr-14 | 30 |
| L03-8124 | L3 - Flooring @ Guest Rooms | 5 | 5 | 21-Apr-14 | 25-Apr-14 | 30 |
| L03-8128 | L3 - Bath Specialties / Tub Glazing | 3 | 3 | 23-Apr-14 | 25-Apr-14 | 31 |
| L03-8130 | L3 - Guest Rooms Substantially Complete | 0 | 0 | | 28-Apr-14 | 30 |

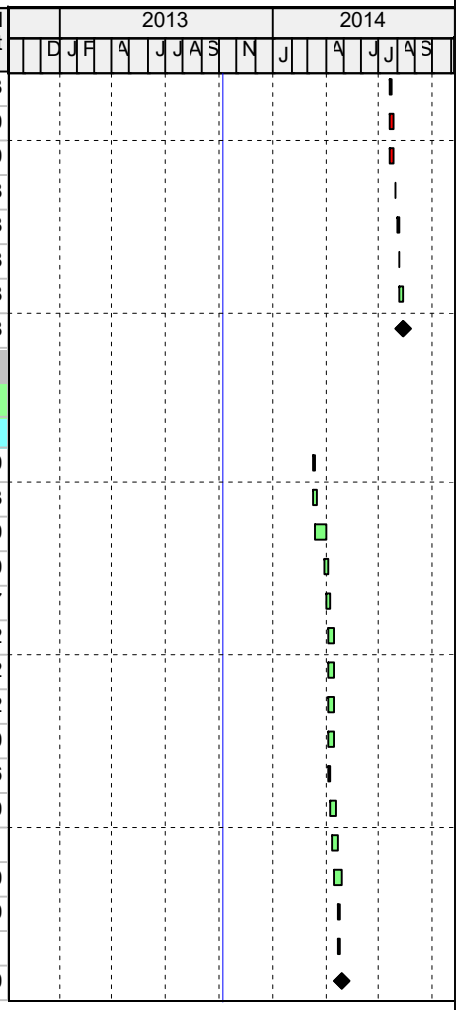



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8114 | L3 - Signage | 3 | 3 | 29-Apr-14 | 01-May-14 | 35 |
| L03-8132 | L3 - Contractor Pre-Punchlist | 5 | 5 | 29-Apr-14 | 05-May-14 | 36 |
| L03-8134 | L3 - Pre-Clean | 5 | 5 | 29-Apr-14 | 05-May-14 | 33 |
| **Pool Area** | | | | | | |
| L03-8216 | L3 - Pool Surfaces / Finishes | 16 | 16 | 21-Aug-14 | 12-Sep-14 | 30 |
| L03-8218 | L3 - Pool Equipment | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 30 |
| **Corridors / Common / Public Areas** | | | | | | |
| L03-8200 | L3 - Final Paint @ Common / Public Areas | 3 | 3 | 29-Apr-14 | 01-May-14 | 30 |
| L03-8202 | L3 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 02-May-14 | 06-May-14 | 30 |
| L03-8204 | L3 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 02-May-14 | 06-May-14 | 30 |
| L03-8206 | L3 - Flooring @ Common / Public Areas | 3 | 3 | 06-May-14 | 08-May-14 | 30 |
| L03-8208 | L3 - Final Clean | 3 | 3 | 09-May-14 | 13-May-14 | 30 |
| L03-8210 | L3 - Owner Walk / Create Punchlist | 1 | 1 | 14-May-14 | 14-May-14 | 30 |
| L03-8212 | L3 - Final Punchlist | 5 | 5 | 15-May-14 | 21-May-14 | 30 |
| L03-8214 | L3 - Floor Complete | 0 | 0 | | 21-May-14 | 30 |
| **Level 4 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L04-8100 | L4 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 18-Mar-14 | 20-Mar-14 | 30 |
| L04-6026 | L4 - Pull Wire | 6 | 6 | 18-Mar-14 | 25-Mar-14 | 53 |
| L04-8102 | L4 - GWB Hang / Tape / Finish - (Including Common / | 14 | 14 | 21-Mar-14 | 09-Apr-14 | 30 |
| L04-8104 | L4 - Int Painting | 5 | 5 | 07-Apr-14 | 11-Apr-14 | 30 |
| L04-8106 | L4 - Wallcoverings | 6 | 6 | 09-Apr-14 | 16-Apr-14 | 37 |
| L04-8108 | L4 - Elec Trim / Finish | 8 | 8 | 14-Apr-14 | 23-Apr-14 | 32 |
| L04-8110 | L4 - HVAC Trim / Finish | 8 | 8 | 14-Apr-14 | 23-Apr-14 | 32 |
| L04-8112 | L4 - Fire Sprinkler Trim / Finish | 8 | 8 | 14-Apr-14 | 23-Apr-14 | 32 |
| L04-8116 | L4 - Finish Carpentry / Millwork | 8 | 8 | 14-Apr-14 | 23-Apr-14 | 30 |
| L04-8118 | L4 - Elec Specialties Trim / Finish | 4 | 4 | 14-Apr-14 | 17-Apr-14 | 36 |

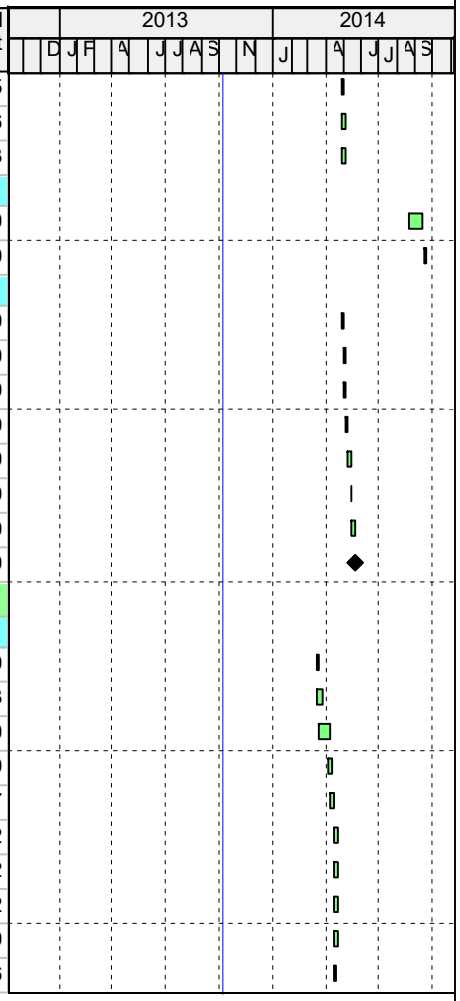



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8120 | L4 - Ceramic Tile / Counter Tops | 8 | 8 | 16-Apr-14 | 25-Apr-14 | 30 |
| L04-8122 | L4 - Plumbing Trim / Finish | 8 | 8 | 18-Apr-14 | 29-Apr-14 | 31 |
| L04-8124 | L4 - Flooring @ Guest Rooms | 5 | 5 | 28-Apr-14 | 02-May-14 | 30 |
| L04-8126 | L4 - Doors & Hardware | 5 | 5 | 29-Apr-14 | 05-May-14 | 30 |
| L04-8128 | L4 - Bath Specialties / Tub Glazing | 3 | 3 | 30-Apr-14 | 02-May-14 | 31 |
| L04-8130 | L4 - Guest Rooms Substantially Complete | 0 | 0 | | 05-May-14 | 30 |
| L04-8114 | L4 - Signage | 3 | 3 | 06-May-14 | 08-May-14 | 35 |
| L04-8132 | L4 - Contractor Pre-Punchlist | 5 | 5 | 06-May-14 | 12-May-14 | 36 |
| L04-8134 | L4 - Pre-Clean | 5 | 5 | 06-May-14 | 12-May-14 | 33 |
| **Corridors / Common / Public Areas** | | | | | | |
| L04-8200 | L4 - Final Paint @ Common / Public Areas | 3 | 3 | 06-May-14 | 08-May-14 | 30 |
| L04-8202 | L4 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 09-May-14 | 13-May-14 | 30 |
| L04-8204 | L4 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 09-May-14 | 13-May-14 | 30 |
| L04-8206 | L4 - Flooring @ Common / Public Areas | 3 | 3 | 13-May-14 | 15-May-14 | 30 |
| L04-8208 | L4 - Final Clean | 3 | 3 | 16-May-14 | 20-May-14 | 30 |
| L04-8210 | L4 - Owner Walk / Create Punchlist | 1 | 1 | 21-May-14 | 21-May-14 | 30 |
| L04-8212 | L4 - Final Punchlist | 5 | 5 | 22-May-14 | 29-May-14 | 30 |
| L04-8214 | L4 - Floor Complete | 0 | 0 | | 29-May-14 | 30 |
| **Level 5 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L05-8100 | L5 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 25-Mar-14 | 27-Mar-14 | 30 |
| L05-6026 | L5 - Pull Wire | 6 | 6 | 25-Mar-14 | 01-Apr-14 | 53 |
| L05-8102 | L5 - GWB Hang / Tape / Finish - (Including Common / | 14 | 14 | 28-Mar-14 | 16-Apr-14 | 30 |
| L05-8104 | L5 - Int Painting | 5 | 5 | 14-Apr-14 | 18-Apr-14 | 30 |
| L05-8106 | L5 - Wallcoverings | 6 | 6 | 16-Apr-14 | 23-Apr-14 | 37 |
| L05-8108 | L5 - Elec Trim / Finish | 8 | 8 | 21-Apr-14 | 30-Apr-14 | 32 |
| L05-8110 | L5 - HVAC Trim / Finish | 8 | 8 | 21-Apr-14 | 30-Apr-14 | 32 |

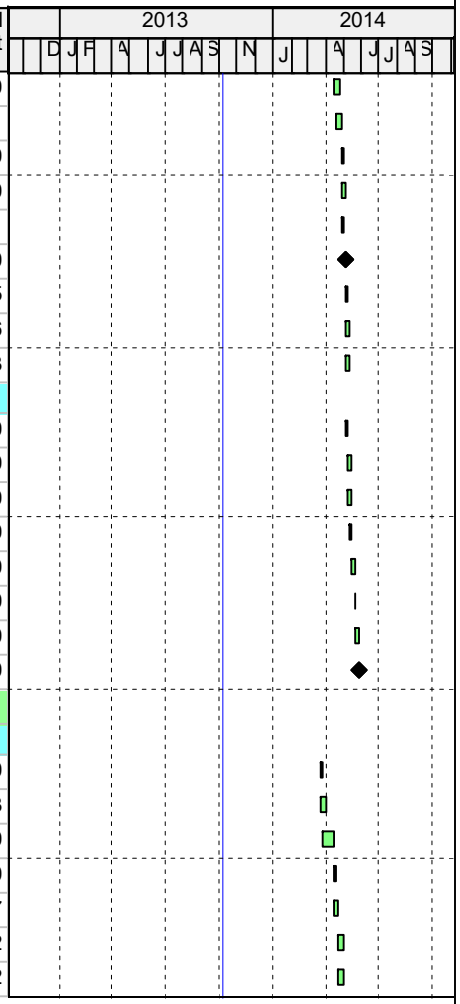



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8112 | L5 - Fire Sprinkler Trim / Finish | 8 | 8 | 21-Apr-14 | 30-Apr-14 | 32 |
| L05-8116 | L5 - Finish Carpentry / Millwork | 8 | 8 | 21-Apr-14 | 30-Apr-14 | 30 |
| L05-8118 | L5 - Elec Specialties Trim / Finish | 4 | 4 | 21-Apr-14 | 24-Apr-14 | 36 |
| L05-8120 | L5 - Ceramic Tile / Counter Tops | 8 | 8 | 23-Apr-14 | 02-May-14 | 30 |
| L05-8122 | L5 - Plumbing Trim / Finish | 8 | 8 | 25-Apr-14 | 06-May-14 | 31 |
| L05-8124 | L5 - Flooring @ Guest Rooms | 5 | 5 | 05-May-14 | 09-May-14 | 30 |
| L05-8126 | L5 - Doors & Hardware | 5 | 5 | 06-May-14 | 12-May-14 | 30 |
| L05-8128 | L5 - Bath Specialties / Tub Glazing | 3 | 3 | 07-May-14 | 09-May-14 | 31 |
| L05-8130 | L5 - Guest Rooms Substantially Complete | 0 | 0 | | 12-May-14 | 30 |
| L05-8114 | L5 - Signage | 3 | 3 | 13-May-14 | 15-May-14 | 35 |
| L05-8132 | L5 - Contractor Pre-Punchlist | 5 | 5 | 13-May-14 | 19-May-14 | 36 |
| L05-8134 | L5 - Pre-Clean | 5 | 5 | 13-May-14 | 19-May-14 | 33 |
| **Corridors / Common / Public Areas** | | | | | | |
| L05-8200 | L5 - Final Paint @ Common / Public Areas | 3 | 3 | 13-May-14 | 15-May-14 | 30 |
| L05-8202 | L5 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 16-May-14 | 20-May-14 | 30 |
| L05-8204 | L5 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 16-May-14 | 20-May-14 | 30 |
| L05-8206 | L5 - Flooring @ Common / Public Areas | 3 | 3 | 20-May-14 | 22-May-14 | 30 |
| L05-8208 | L5 - Final Clean | 3 | 3 | 23-May-14 | 28-May-14 | 30 |
| L05-8210 | L5 - Owner Walk / Create Punchlist | 1 | 1 | 29-May-14 | 29-May-14 | 30 |
| L05-8212 | L5 - Final Punchlist | 5 | 5 | 30-May-14 | 05-Jun-14 | 30 |
| L05-8214 | L5 - Floor Complete | 0 | 0 | | 05-Jun-14 | 30 |
| **Level 6 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L06-8100 | L6 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 01-Apr-14 | 03-Apr-14 | 30 |
| L06-6026 | L6 - Pull Wire | 6 | 6 | 01-Apr-14 | 08-Apr-14 | 53 |
| L06-8102 | L6 - GWB Hang / Tape / Finish - (Including Common / | 14 | 14 | 04-Apr-14 | 23-Apr-14 | 30 |
| L06-8104 | L6 - Int Painting | 5 | 5 | 21-Apr-14 | 25-Apr-14 | 30 |

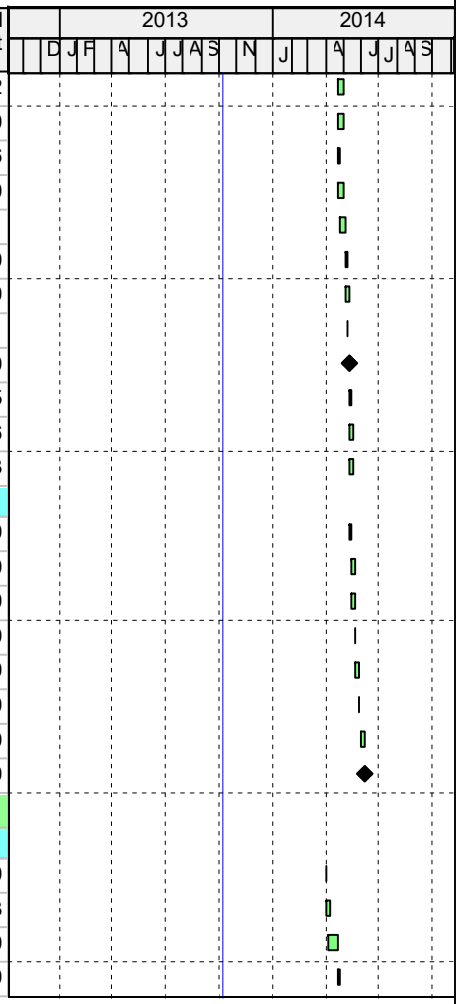



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8106 | L6 - Wallcoverings | 6 | 6 | 23-Apr-14 | 30-Apr-14 | 37 |
| L06-8108 | L6 - Elec Trim / Finish | 8 | 8 | 28-Apr-14 | 07-May-14 | 32 |
| L06-8110 | L6 - HVAC Trim / Finish | 8 | 8 | 28-Apr-14 | 07-May-14 | 32 |
| L06-8112 | L6 - Fire Sprinkler Trim / Finish | 8 | 8 | 28-Apr-14 | 07-May-14 | 32 |
| L06-8116 | L6 - Finish Carpentry / Millwork | 8 | 8 | 28-Apr-14 | 07-May-14 | 30 |
| L06-8118 | L6 - Elec Specialties Trim / Finish | 4 | 4 | 28-Apr-14 | 01-May-14 | 36 |
| L06-8120 | L6 - Ceramic Tile / Counter Tops | 8 | 8 | 30-Apr-14 | 09-May-14 | 30 |
| L06-8122 | L6 - Plumbing Trim / Finish | 8 | 8 | 02-May-14 | 13-May-14 | 31 |
| L06-8124 | L6 - Flooring @ Guest Rooms | 5 | 5 | 12-May-14 | 16-May-14 | 30 |
| L06-8126 | L6 - Doors & Hardware | 5 | 5 | 13-May-14 | 19-May-14 | 30 |
| L06-8128 | L6 - Bath Specialties / Tub Glazing | 3 | 3 | 14-May-14 | 16-May-14 | 31 |
| L06-8130 | L6 - Guest Rooms Substantially Complete | 0 | 0 | | 19-May-14 | 30 |
| L06-8114 | L6 - Signage | 3 | 3 | 20-May-14 | 22-May-14 | 35 |
| L06-8132 | L6 - Contractor Pre-Punchlist | 5 | 5 | 20-May-14 | 27-May-14 | 36 |
| L06-8134 | L6 - Pre-Clean | 5 | 5 | 20-May-14 | 27-May-14 | 33 |
| **Corridors / Common / Public Areas** | | | | | | |
| L06-8200 | L6 - Final Paint @ Common / Public Areas | 3 | 3 | 20-May-14 | 22-May-14 | 30 |
| L06-8202 | L6 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 23-May-14 | 28-May-14 | 30 |
| L06-8204 | L6 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 23-May-14 | 28-May-14 | 30 |
| L06-8206 | L6 - Flooring @ Common / Public Areas | 3 | 3 | 28-May-14 | 30-May-14 | 30 |
| L06-8208 | L6 - Final Clean | 3 | 3 | 02-Jun-14 | 04-Jun-14 | 30 |
| L06-8210 | L6 - Owner Walk / Create Punchlist | 1 | 1 | 05-Jun-14 | 05-Jun-14 | 30 |
| L06-8212 | L6 - Final Punchlist | 5 | 5 | 06-Jun-14 | 12-Jun-14 | 30 |
| L06-8214 | L6 - Floor Complete | 0 | 0 | | 12-Jun-14 | 30 |
| **Level 7 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L07-8100 | L7 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 08-Apr-14 | 10-Apr-14 | 30 |

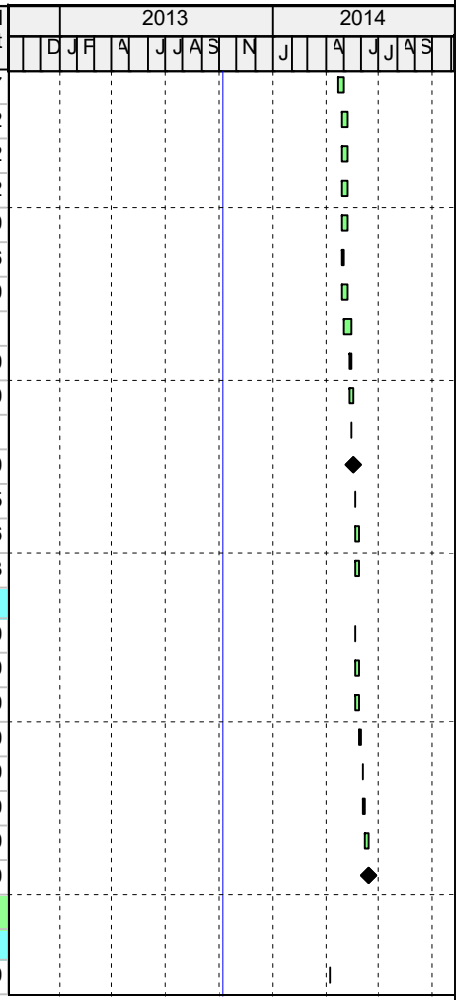



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6026 | L7 - Pull Wire | 6 | 6 | 08-Apr-14 | 15-Apr-14 | 53 |
| L07-8102 | L7 - GWB Hang / Tape / Finish - (Including Common / | 14 | 14 | 11-Apr-14 | 30-Apr-14 | 30 |
| L07-8104 | L7 - Int Painting | 5 | 5 | 28-Apr-14 | 02-May-14 | 30 |
| L07-8106 | L7 - Wallcoverings | 6 | 6 | 30-Apr-14 | 07-May-14 | 37 |
| L07-8108 | L7 - Elec Trim / Finish | 8 | 8 | 05-May-14 | 14-May-14 | 32 |
| L07-8110 | L7 - HVAC Trim / Finish | 8 | 8 | 05-May-14 | 14-May-14 | 32 |
| L07-8112 | L7 - Fire Sprinkler Trim / Finish | 8 | 8 | 05-May-14 | 14-May-14 | 32 |
| L07-8116 | L7 - Finish Carpentry / Millwork | 8 | 8 | 05-May-14 | 14-May-14 | 30 |
| L07-8118 | L7 - Elec Specialties Trim / Finish | 4 | 4 | 05-May-14 | 08-May-14 | 36 |
| L07-8120 | L7 - Ceramic Tile / Counter Tops | 8 | 8 | 07-May-14 | 16-May-14 | 30 |
| L07-8122 | L7 - Plumbing Trim / Finish | 8 | 8 | 09-May-14 | 20-May-14 | 31 |
| L07-8124 | L7 - Flooring @ Guest Rooms | 5 | 5 | 19-May-14 | 23-May-14 | 30 |
| L07-8126 | L7 - Doors & Hardware | 5 | 5 | 20-May-14 | 27-May-14 | 30 |
| L07-8128 | L7 - Bath Specialties / Tub Glazing | 3 | 3 | 21-May-14 | 23-May-14 | 31 |
| L07-8130 | L7 - Guest Rooms Substantially Complete | 0 | 0 | | 27-May-14 | 30 |
| L07-8114 | L7 - Signage | 3 | 3 | 28-May-14 | 30-May-14 | 35 |
| L07-8132 | L7 - Contractor Pre-Punchlist | 5 | 5 | 28-May-14 | 03-Jun-14 | 36 |
| L07-8134 | L7 - Pre-Clean | 5 | 5 | 28-May-14 | 03-Jun-14 | 33 |
| **Corridors / Common / Public Areas** | | | | | | |
| L07-8200 | L7 - Final Paint @ Common / Public Areas | 3 | 3 | 28-May-14 | 30-May-14 | 30 |
| L07-8202 | L7 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 02-Jun-14 | 04-Jun-14 | 30 |
| L07-8204 | L7 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 02-Jun-14 | 04-Jun-14 | 30 |
| L07-8206 | L7 - Flooring @ Common / Public Areas | 3 | 3 | 04-Jun-14 | 06-Jun-14 | 30 |
| L07-8208 | L7 - Final Clean | 3 | 3 | 09-Jun-14 | 11-Jun-14 | 30 |
| L07-8210 | L7 - Owner Walk / Create Punchlist | 1 | 1 | 12-Jun-14 | 12-Jun-14 | 30 |
| L07-8212 | L7 - Final Punchlist | 5 | 5 | 13-Jun-14 | 19-Jun-14 | 30 |
| L07-8214 | L7 - Floor Complete | 0 | 0 | | 19-Jun-14 | 30 |

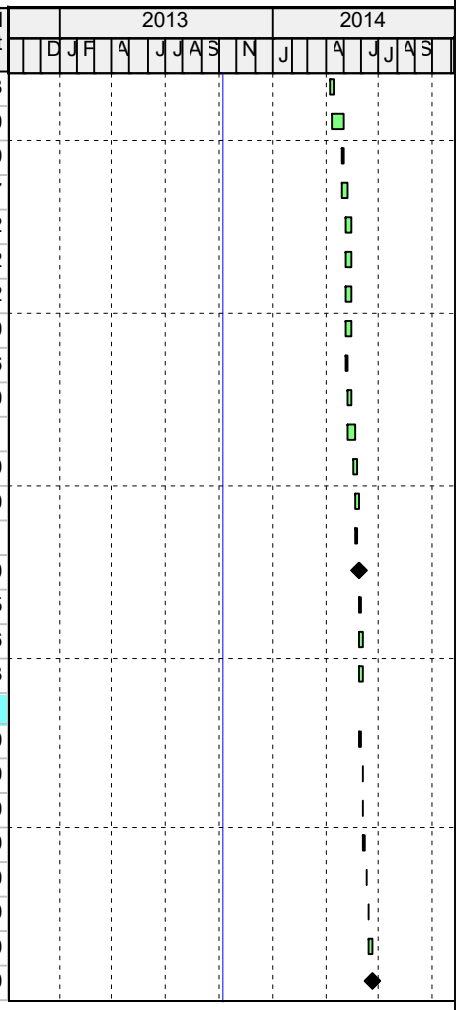



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Level 8 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L08-8100 | L8 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 15-Apr-14 | 17-Apr-14 | 30 |
| L08-6026 | L8 - Pull Wire | 6 | 6 | 15-Apr-14 | 22-Apr-14 | 53 |
| L08-8102 | L8 - GWB Hang / Tape / Finish - (Including Common / | 14 | 14 | 18-Apr-14 | 07-May-14 | 30 |
| L08-8104 | L8 - Int Painting | 5 | 5 | 05-May-14 | 09-May-14 | 30 |
| L08-8106 | L8 - Wallcoverings | 6 | 6 | 07-May-14 | 14-May-14 | 37 |
| L08-8108 | L8 - Elec Trim / Finish | 8 | 8 | 12-May-14 | 21-May-14 | 32 |
| L08-8110 | L8 - HVAC Trim / Finish | 8 | 8 | 12-May-14 | 21-May-14 | 32 |
| L08-8112 | L8 - Fire Sprinkler Trim / Finish | 8 | 8 | 12-May-14 | 21-May-14 | 32 |
| L08-8116 | L8 - Finish Carpentry / Millwork | 8 | 8 | 12-May-14 | 21-May-14 | 30 |
| L08-8118 | L8 - Elec Specialties Trim / Finish | 4 | 4 | 12-May-14 | 15-May-14 | 36 |
| L08-8120 | L8 - Ceramic Tile / Counter Tops | 8 | 8 | 14-May-14 | 23-May-14 | 30 |
| L08-8122 | L8 - Plumbing Trim / Finish | 8 | 8 | 16-May-14 | 28-May-14 | 31 |
| L08-8124 | L8 - Flooring @ Guest Rooms | 5 | 5 | 27-May-14 | 02-Jun-14 | 30 |
| L08-8126 | L8 - Doors & Hardware | 5 | 5 | 28-May-14 | 03-Jun-14 | 30 |
| L08-8128 | L8 - Bath Specialties / Tub Glazing | 3 | 3 | 29-May-14 | 02-Jun-14 | 31 |
| L08-8130 | L8 - Guest Rooms Substantially Complete | 0 | 0 | | 03-Jun-14 | 30 |
| L08-8114 | L8 - Signage | 3 | 3 | 04-Jun-14 | 06-Jun-14 | 35 |
| L08-8132 | L8 - Contractor Pre-Punchlist | 5 | 5 | 04-Jun-14 | 10-Jun-14 | 36 |
| L08-8134 | L8 - Pre-Clean | 5 | 5 | 04-Jun-14 | 10-Jun-14 | 33 |
| **Corridors / Common / Public Areas** | | | | | | |
| L08-8200 | L8 - Final Paint @ Common / Public Areas | 3 | 3 | 04-Jun-14 | 06-Jun-14 | 30 |
| L08-8202 | L8 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 09-Jun-14 | 11-Jun-14 | 30 |
| L08-8204 | L8 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 09-Jun-14 | 11-Jun-14 | 30 |
| L08-8206 | L8 - Flooring @ Common / Public Areas | 3 | 3 | 11-Jun-14 | 13-Jun-14 | 30 |
| L08-8208 | L8 - Final Clean | 3 | 3 | 16-Jun-14 | 18-Jun-14 | 30 |

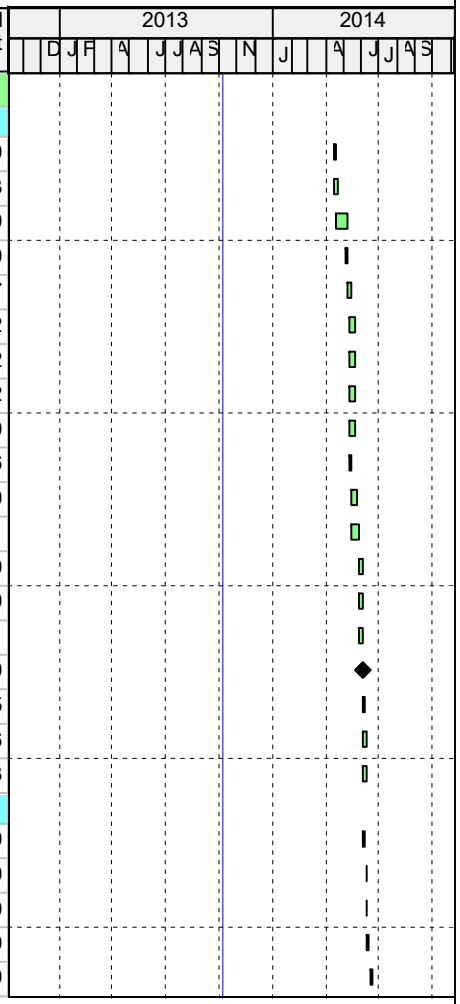



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8210 | L8 - Owner Walk / Create Punchlist | 1 | 1 | 19-Jun-14 | 19-Jun-14 | 30 |
| L08-8212 | L8 - Final Punchlist | 5 | 5 | 20-Jun-14 | 26-Jun-14 | 30 |
| L08-8214 | L8 - Floor Complete | 0 | 0 | | 26-Jun-14 | 30 |
| **Level 9 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L09-8100 | L9 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 22-Apr-14 | 24-Apr-14 | 30 |
| L09-6026 | L9 - Pull Wire | 6 | 6 | 22-Apr-14 | 29-Apr-14 | 53 |
| L09-8102 | L9 - GWB Hang / Tape / Finish - (Including Common / | 14 | 14 | 25-Apr-14 | 14-May-14 | 30 |
| L09-8104 | L9 - Int Painting | 5 | 5 | 12-May-14 | 16-May-14 | 30 |
| L09-8106 | L9 - Wallcoverings | 6 | 6 | 14-May-14 | 21-May-14 | 37 |
| L09-8108 | L9 - Elec Trim / Finish | 8 | 8 | 19-May-14 | 29-May-14 | 32 |
| L09-8110 | L9 - HVAC Trim / Finish | 8 | 8 | 19-May-14 | 29-May-14 | 32 |
| L09-8112 | L9 - Fire Sprinkler Trim / Finish | 8 | 8 | 19-May-14 | 29-May-14 | 32 |
| L09-8116 | L9 - Finish Carpentry / Millwork | 8 | 8 | 19-May-14 | 29-May-14 | 30 |
| L09-8118 | L9 - Elec Specialties Trim / Finish | 4 | 4 | 19-May-14 | 22-May-14 | 36 |
| L09-8120 | L9 - Ceramic Tile / Counter Tops | 8 | 8 | 21-May-14 | 02-Jun-14 | 30 |
| L09-8122 | L9 - Plumbing Trim / Finish | 8 | 8 | 23-May-14 | 04-Jun-14 | 31 |
| L09-8124 | L9 - Flooring @ Guest Rooms | 5 | 5 | 03-Jun-14 | 09-Jun-14 | 30 |
| L09-8126 | L9 - Doors & Hardware | 5 | 5 | 04-Jun-14 | 10-Jun-14 | 30 |
| L09-8128 | L9 - Bath Specialties / Tub Glazing | 3 | 3 | 05-Jun-14 | 09-Jun-14 | 31 |
| L09-8130 | L9 - Guest Rooms Substantially Complete | 0 | 0 | | 10-Jun-14 | 30 |
| L09-8114 | L9 - Signage | 3 | 3 | 11-Jun-14 | 13-Jun-14 | 35 |
| L09-8132 | L9 - Contractor Pre-Punchlist | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 36 |
| L09-8134 | L9 - Pre-Clean | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 33 |
| **Corridors / Common / Public Areas** | | | | | | |
| L09-8200 | L9 - Final Paint @ Common / Public Areas | 3 | 3 | 11-Jun-14 | 13-Jun-14 | 30 |
| L09-8202 | L9 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 16-Jun-14 | 18-Jun-14 | 30 |

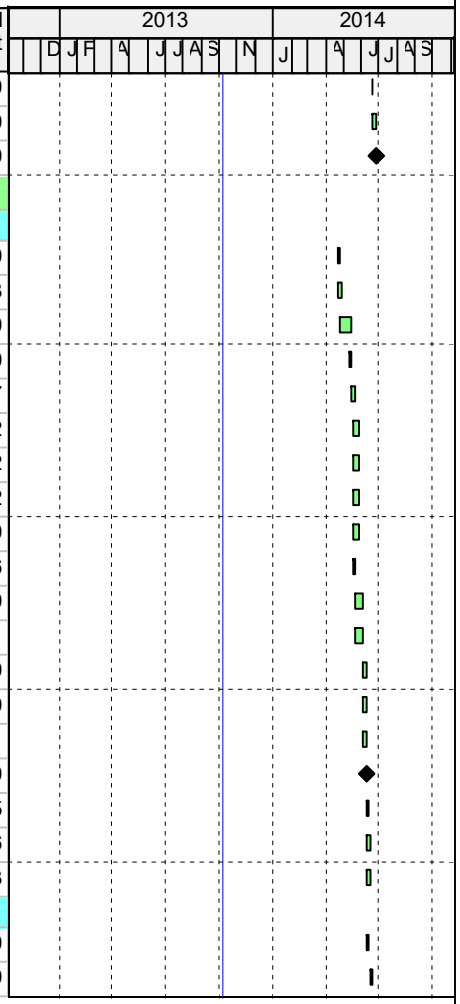



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8204 | L9 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 16-Jun-14 | 18-Jun-14 | 30 |
| L09-8206 | L9 - Flooring @ Common / Public Areas | 3 | 3 | 18-Jun-14 | 20-Jun-14 | 30 |
| L09-8208 | L9 - Final Clean | 3 | 3 | 23-Jun-14 | 25-Jun-14 | 30 |
| L09-8210 | L9 - Owner Walk / Create Punchlist | 1 | 1 | 26-Jun-14 | 26-Jun-14 | 30 |
| L09-8212 | L9 - Final Punchlist | 5 | 5 | 27-Jun-14 | 03-Jul-14 | 30 |
| L09-8214 | L9 - Floor Complete | 0 | 0 | | 03-Jul-14 | 30 |
| **Level 10 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L10-8100 | L10 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 29-Apr-14 | 01-May-14 | 30 |
| L10-6026 | L10 - Pull Wire | 6 | 6 | 29-Apr-14 | 06-May-14 | 53 |
| L10-8102 | L10 - GWB Hang / Tape / Finish - (Including Commor | 14 | 14 | 02-May-14 | 21-May-14 | 30 |
| L10-8104 | L10 - Int Painting | 5 | 5 | 19-May-14 | 23-May-14 | 30 |
| L10-8106 | L10 - Wallcoverings | 6 | 6 | 21-May-14 | 29-May-14 | 37 |
| L10-8108 | L10 - Elec Trim / Finish | 8 | 8 | 27-May-14 | 05-Jun-14 | 32 |
| L10-8110 | L10 - HVAC Trim / Finish | 8 | 8 | 27-May-14 | 05-Jun-14 | 32 |
| L10-8112 | L10 - Fire Sprinkler Trim / Finish | 8 | 8 | 27-May-14 | 05-Jun-14 | 32 |
| L10-8116 | L10 - Finish Carpentry / Millwork | 8 | 8 | 27-May-14 | 05-Jun-14 | 30 |
| L10-8118 | L10 - Elec Specialties Trim / Finish | 4 | 4 | 27-May-14 | 30-May-14 | 36 |
| L10-8120 | L10 - Ceramic Tile / Counter Tops | 8 | 8 | 29-May-14 | 09-Jun-14 | 30 |
| L10-8122 | L10 - Plumbing Trim / Finish | 8 | 8 | 02-Jun-14 | 11-Jun-14 | 31 |
| L10-8124 | L10 - Flooring @ Guest Rooms | 5 | 5 | 10-Jun-14 | 16-Jun-14 | 30 |
| L10-8126 | L10 - Doors & Hardware | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 30 |
| L10-8128 | L10 - Bath Specialties / Tub Glazing | 3 | 3 | 12-Jun-14 | 16-Jun-14 | 31 |
| L10-8130 | L10 - Guest Rooms Substantially Complete | 0 | 0 | | 17-Jun-14 | 30 |
| L10-8114 | L10 - Signage | 3 | 3 | 18-Jun-14 | 20-Jun-14 | 35 |
| L10-8132 | L10 - Contractor Pre-Punchlist | 5 | 5 | 18-Jun-14 | 24-Jun-14 | 36 |
| L10-8134 | L10 - Pre-Clean | 5 | 5 | 18-Jun-14 | 24-Jun-14 | 33 |

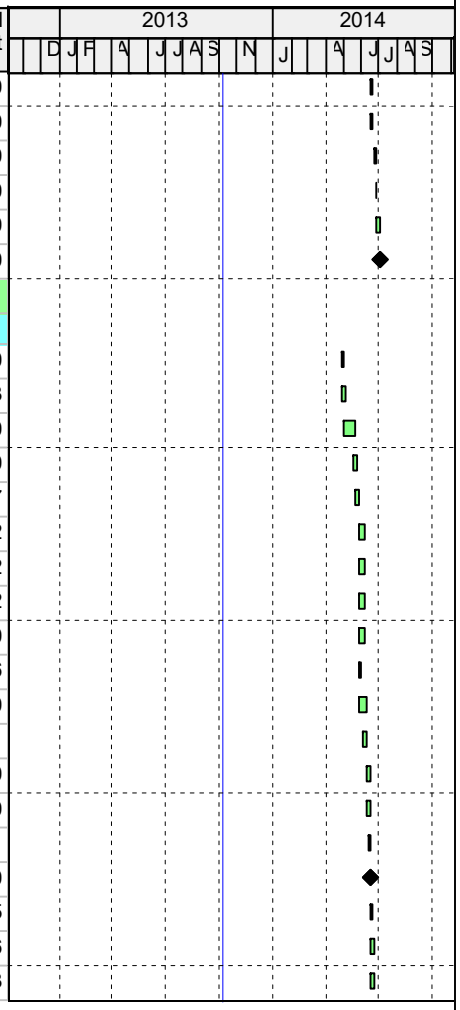



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Corridors / Common / Public Areas** | | | | | | |
| L10-8200 | L10 - Final Paint @ Common / Public Areas | 3 | 3 | 18-Jun-14 | 20-Jun-14 | 30 |
| L10-8202 | L10 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 23-Jun-14 | 25-Jun-14 | 30 |
| L10-8204 | L10 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 23-Jun-14 | 25-Jun-14 | 30 |
| L10-8206 | L10 - Flooring @ Common / Public Areas | 3 | 3 | 25-Jun-14 | 27-Jun-14 | 30 |
| L10-8208 | L10 - Final Clean | 3 | 3 | 30-Jun-14 | 02-Jul-14 | 30 |
| L10-8210 | L10 - Owner Walk / Create Punchlist | 1 | 1 | 03-Jul-14 | 03-Jul-14 | 30 |
| L10-8212 | L10 - Final Punchlist | 5 | 5 | 07-Jul-14 | 11-Jul-14 | 30 |
| L10-8214 | L10 - Floor Complete | 0 | 0 | | 11-Jul-14 | 30 |
| **Level 11 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L11-8100 | L11 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 06-May-14 | 08-May-14 | 49 |
| L11-6026 | L11 - Pull Wire | 6 | 6 | 06-May-14 | 13-May-14 | 72 |
| L11-8102 | L11 - GWB Hang / Tape / Finish - (Including Common | 14 | 14 | 09-May-14 | 29-May-14 | 49 |
| L11-8104 | L11 - Int Painting | 5 | 5 | 27-May-14 | 02-Jun-14 | 49 |
| L11-8106 | L11 - Wallcoverings | 6 | 6 | 29-May-14 | 05-Jun-14 | 56 |
| L11-8108 | L11 - Elec Trim / Finish | 8 | 8 | 03-Jun-14 | 12-Jun-14 | 51 |
| L11-8110 | L11 - HVAC Trim / Finish | 8 | 8 | 03-Jun-14 | 12-Jun-14 | 51 |
| L11-8112 | L11 - Fire Sprinkler Trim / Finish | 8 | 8 | 03-Jun-14 | 12-Jun-14 | 51 |
| L11-8116 | L11 - Finish Carpentry / Millwork | 8 | 8 | 03-Jun-14 | 12-Jun-14 | 49 |
| L11-8118 | L11 - Elec Specialties Trim / Finish | 4 | 4 | 03-Jun-14 | 06-Jun-14 | 55 |
| L11-8120 | L11 - Ceramic Tile / Counter Tops | 8 | 8 | 05-Jun-14 | 16-Jun-14 | 49 |
| L11-8122 | L11 - Plumbing Trim / Finish | 8 | 8 | 09-Jun-14 | 18-Jun-14 | 50 |
| L11-8124 | L11 - Flooring @ Guest Rooms | 5 | 5 | 17-Jun-14 | 23-Jun-14 | 49 |
| L11-8126 | L11 - Doors & Hardware | 5 | 5 | 18-Jun-14 | 24-Jun-14 | 49 |
| L11-8128 | L11 - Bath Specialties / Tub Glazing | 3 | 3 | 19-Jun-14 | 23-Jun-14 | 50 |
| L11-8130 | L11 - Guest Rooms Substantially Complete | 0 | 0 | | 24-Jun-14 | 49 |

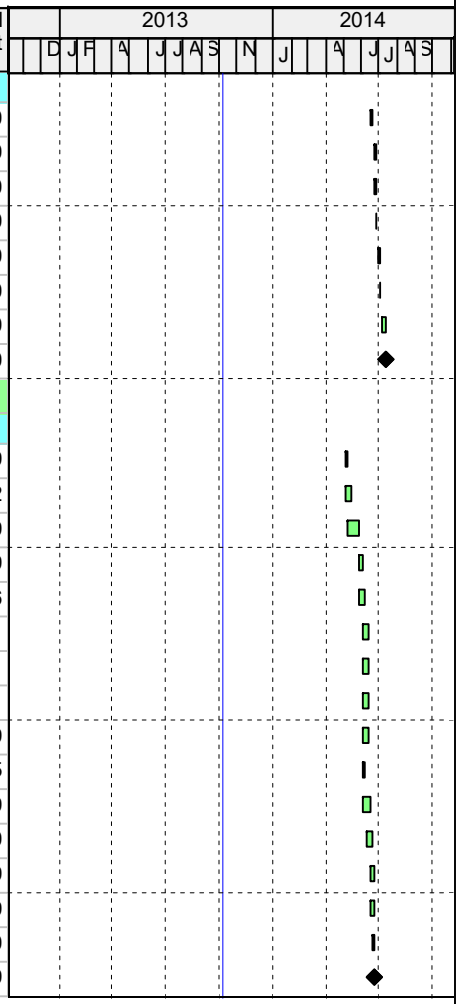



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8114 | L11 - Signage | 3 | 3 | 25-Jun-14 | 27-Jun-14 | 54 |
| L11-8132 | L11 - Contractor Pre-Punchlist | 5 | 5 | 25-Jun-14 | 01-Jul-14 | 55 |
| L11-8134 | L11 - Pre-Clean | 5 | 5 | 25-Jun-14 | 01-Jul-14 | 52 |
| **Corridors / Common / Public Areas** | | | | | | |
| L11-8200 | L11 - Final Paint @ Common / Public Areas | 3 | 3 | 25-Jun-14 | 27-Jun-14 | 49 |
| L11-8202 | L11 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 30-Jun-14 | 02-Jul-14 | 49 |
| L11-8204 | L11 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 30-Jun-14 | 02-Jul-14 | 49 |
| L11-8206 | L11 - Flooring @ Common / Public Areas | 3 | 3 | 02-Jul-14 | 07-Jul-14 | 49 |
| L11-8208 | L11 - Final Clean | 3 | 3 | 08-Jul-14 | 10-Jul-14 | 49 |
| L11-8210 | L11 - Owner Walk / Create Punchlist | 1 | 1 | 11-Jul-14 | 11-Jul-14 | 49 |
| L11-8212 | L11 - Final Punchlist | 5 | 5 | 14-Jul-14 | 18-Jul-14 | 49 |
| L11-8214 | L11 - Floor Complete | 0 | 0 | | 18-Jul-14 | 49 |
| **Level 12 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L12-8100 | L12 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 20-May-14 | 22-May-14 | 44 |
| L12-6026 | L12 - Pull Wire | 6 | 6 | 20-May-14 | 28-May-14 | 67 |
| L12-8102 | L12 - GWB Hang / Tape / Finish - (Including Commor | 14 | 14 | 23-May-14 | 12-Jun-14 | 44 |
| L12-8104 | L12 - Int Painting | 5 | 5 | 10-Jun-14 | 16-Jun-14 | 44 |
| L12-8106 | L12 - Wallcoverings | 6 | 6 | 12-Jun-14 | 19-Jun-14 | 51 |
| L12-8108 | L12 - Elec Trim / Finish | 8 | 8 | 17-Jun-14 | 26-Jun-14 | 46 |
| L12-8110 | L12 - HVAC Trim / Finish | 8 | 8 | 17-Jun-14 | 26-Jun-14 | 46 |
| L12-8112 | L12 - Fire Sprinkler Trim / Finish | 8 | 8 | 17-Jun-14 | 26-Jun-14 | 46 |
| L12-8116 | L12 - Finish Carpentry / Millwork | 8 | 8 | 17-Jun-14 | 26-Jun-14 | 44 |
| L12-8118 | L12 - Elec Specialties Trim / Finish | 4 | 4 | 17-Jun-14 | 20-Jun-14 | 50 |
| L12-8120 | L12 - Ceramic Tile / Counter Tops | 8 | 8 | 19-Jun-14 | 30-Jun-14 | 44 |
| L12-8122 | L12 - Plumbing Trim / Finish | 8 | 8 | 23-Jun-14 | 02-Jul-14 | 45 |
| L12-8124 | L12 - Flooring @ Guest Rooms | 5 | 5 | 01-Jul-14 | 08-Jul-14 | 44 |

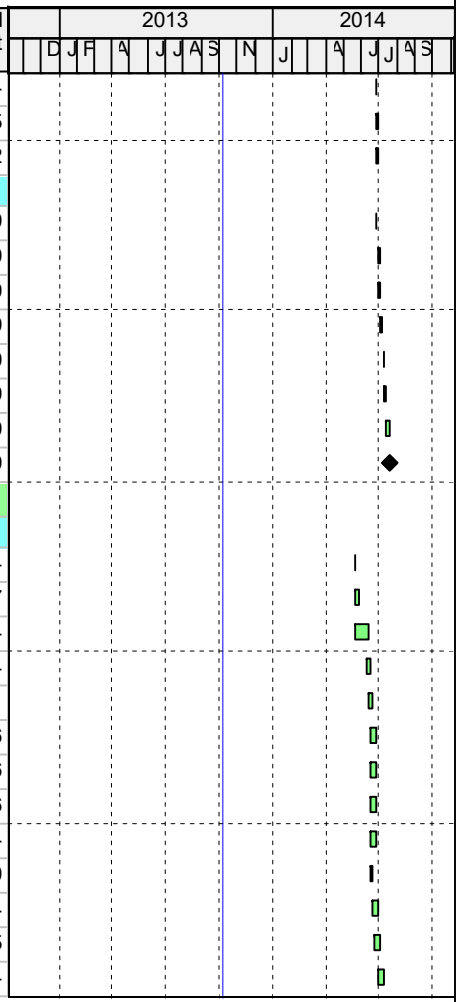



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8126 | L12 - Doors & Hardware | 5 | 5 | 02-Jul-14 | 09-Jul-14 | 44 |
| L12-8128 | L12 - Bath Specialties / Tub Glazing | 3 | 3 | 03-Jul-14 | 08-Jul-14 | 45 |
| L12-8130 | L12 - Guest Rooms Substantially Complete | 0 | 0 | | 09-Jul-14 | 44 |
| L12-8114 | L12 - Signage | 3 | 3 | 10-Jul-14 | 14-Jul-14 | 49 |
| L12-8132 | L12 - Contractor Pre-Punchlist | 5 | 5 | 10-Jul-14 | 16-Jul-14 | 50 |
| L12-8134 | L12 - Pre-Clean | 5 | 5 | 10-Jul-14 | 16-Jul-14 | 47 |
| **Corridors / Common / Public Areas** | | | | | | |
| L12-8200 | L12 - Final Paint @ Common / Public Areas | 3 | 3 | 10-Jul-14 | 14-Jul-14 | 44 |
| L12-8202 | L12 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 15-Jul-14 | 17-Jul-14 | 44 |
| L12-8204 | L12 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 15-Jul-14 | 17-Jul-14 | 44 |
| L12-8206 | L12 - Flooring @ Common / Public Areas | 3 | 3 | 17-Jul-14 | 21-Jul-14 | 44 |
| L12-8208 | L12 - Final Clean | 3 | 3 | 22-Jul-14 | 24-Jul-14 | 44 |
| L12-8210 | L12 - Owner Walk / Create Punchlist | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 44 |
| L12-8212 | L12 - Final Punchlist | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 44 |
| L12-8214 | L12 - Floor Complete | 0 | 0 | | 01-Aug-14 | 44 |
| **Level 14 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L14-8100 | L14 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 22-May-14 | 27-May-14 | 47 |
| L14-6026 | L14 - Pull Wire | 6 | 6 | 22-May-14 | 30-May-14 | 70 |
| L14-8102 | L14 - GWB Hang / Tape / Finish - (Including Commor | 14 | 14 | 02-Jun-14 | 19-Jun-14 | 44 |
| L14-8104 | L14 - Int Painting | 5 | 5 | 17-Jun-14 | 23-Jun-14 | 44 |
| L14-8106 | L14 - Wallcoverings | 6 | 6 | 19-Jun-14 | 26-Jun-14 | 51 |
| L14-8108 | L14 - Elec Trim / Finish | 8 | 8 | 24-Jun-14 | 03-Jul-14 | 46 |
| L14-8110 | L14 - HVAC Trim / Finish | 8 | 8 | 24-Jun-14 | 03-Jul-14 | 46 |
| L14-8112 | L14 - Fire Sprinkler Trim / Finish | 8 | 8 | 24-Jun-14 | 03-Jul-14 | 46 |
| L14-8116 | L14 - Finish Carpentry / Millwork | 8 | 8 | 24-Jun-14 | 03-Jul-14 | 44 |
| L14-8118 | L14 - Elec Specialties Trim / Finish | 4 | 4 | 24-Jun-14 | 27-Jun-14 | 50 |

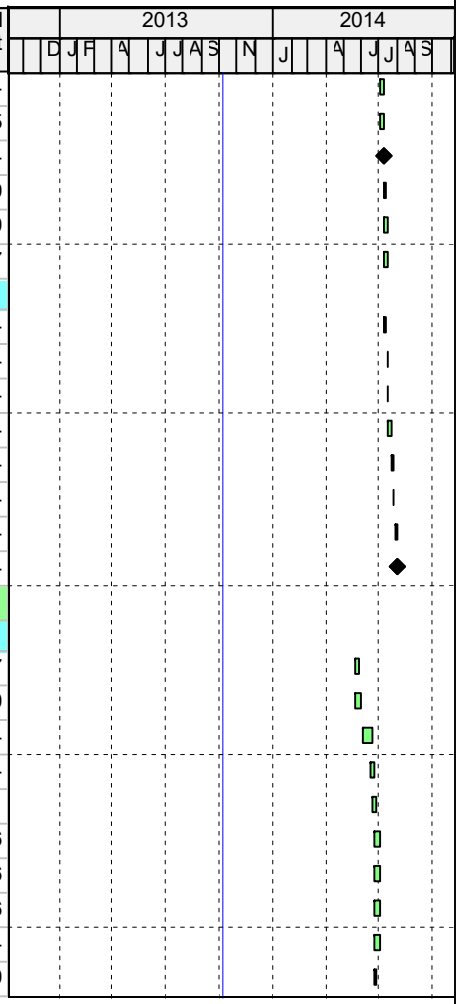



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8120 | L14 - Ceramic Tile / Counter Tops | 8 | 8 | 26-Jun-14 | 08-Jul-14 | 44 |
| L14-8122 | L14 - Plumbing Trim / Finish | 8 | 8 | 30-Jun-14 | 10-Jul-14 | 45 |
| L14-8124 | L14 - Flooring @ Guest Rooms | 5 | 5 | 09-Jul-14 | 15-Jul-14 | 44 |
| L14-8126 | L14 - Doors & Hardware | 5 | 5 | 10-Jul-14 | 16-Jul-14 | 44 |
| L14-8128 | L14 - Bath Specialties / Tub Glazing | 3 | 3 | 11-Jul-14 | 15-Jul-14 | 45 |
| L14-8130 | L14 - Guest Rooms Substantially Complete | 0 | 0 | | 16-Jul-14 | 44 |
| L14-8114 | L14 - Signage | 3 | 3 | 17-Jul-14 | 21-Jul-14 | 49 |
| L14-8132 | L14 - Contractor Pre-Punchlist | 5 | 5 | 17-Jul-14 | 23-Jul-14 | 50 |
| L14-8134 | L14 - Pre-Clean | 5 | 5 | 17-Jul-14 | 23-Jul-14 | 47 |
| **Corridors / Common / Public Areas** | | | | | | |
| L14-8200 | L14 - Final Paint @ Common / Public Areas | 3 | 3 | 17-Jul-14 | 21-Jul-14 | 44 |
| L14-8202 | L14 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 22-Jul-14 | 24-Jul-14 | 44 |
| L14-8204 | L14 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 22-Jul-14 | 24-Jul-14 | 44 |
| L14-8206 | L14 - Flooring @ Common / Public Areas | 3 | 3 | 24-Jul-14 | 28-Jul-14 | 44 |
| L14-8208 | L14 - Final Clean | 3 | 3 | 29-Jul-14 | 31-Jul-14 | 44 |
| L14-8210 | L14 - Owner Walk / Create Punchlist | 1 | 1 | 01-Aug-14 | 01-Aug-14 | 44 |
| L14-8212 | L14 - Final Punchlist | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 44 |
| L14-8214 | L14 - Floor Complete | 0 | 0 | | 08-Aug-14 | 44 |
| **Level 15 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L15-8100 | L15 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 27-May-14 | 29-May-14 | 50 |
| L15-6026 | L15 - Pull Wire | 6 | 6 | 27-May-14 | 03-Jun-14 | 73 |
| L15-8102 | L15 - GWB Hang / Tape / Finish - (Including Commor | 14 | 14 | 09-Jun-14 | 26-Jun-14 | 44 |
| L15-8104 | L15 - Int Painting | 5 | 5 | 24-Jun-14 | 30-Jun-14 | 44 |
| L15-8106 | L15 - Wallcoverings | 6 | 6 | 26-Jun-14 | 03-Jul-14 | 51 |
| L15-8108 | L15 - Elec Trim / Finish | 8 | 8 | 01-Jul-14 | 11-Jul-14 | 46 |
| L15-8110 | L15 - HVAC Trim / Finish | 8 | 8 | 01-Jul-14 | 11-Jul-14 | 46 |

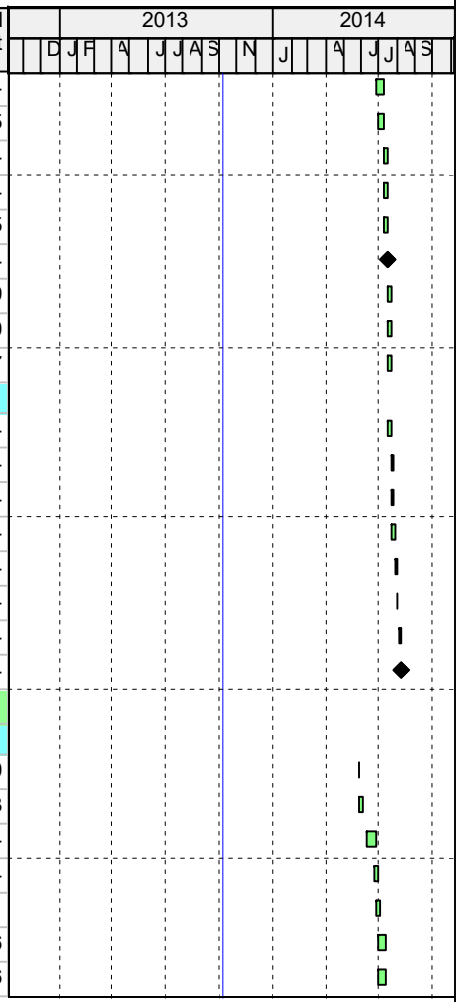



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8112 | L15 - Fire Sprinkler Trim / Finish | 8 | 8 | 01-Jul-14 | 11-Jul-14 | 46 |
| L15-8116 | L15 - Finish Carpentry / Millwork | 8 | 8 | 01-Jul-14 | 11-Jul-14 | 44 |
| L15-8118 | L15 - Elec Specialties Trim / Finish | 4 | 4 | 01-Jul-14 | 07-Jul-14 | 50 |
| L15-8120 | L15 - Ceramic Tile / Counter Tops | 8 | 8 | 03-Jul-14 | 15-Jul-14 | 44 |
| L15-8122 | L15 - Plumbing Trim / Finish | 8 | 8 | 08-Jul-14 | 17-Jul-14 | 45 |
| L15-8124 | L15 - Flooring @ Guest Rooms | 5 | 5 | 16-Jul-14 | 22-Jul-14 | 44 |
| L15-8126 | L15 - Doors & Hardware | 5 | 5 | 17-Jul-14 | 23-Jul-14 | 44 |
| L15-8128 | L15 - Bath Specialties / Tub Glazing | 3 | 3 | 18-Jul-14 | 22-Jul-14 | 45 |
| L15-8130 | L15 - Guest Rooms Substantially Complete | 0 | 0 | | 23-Jul-14 | 44 |
| L15-8114 | L15 - Signage | 3 | 3 | 24-Jul-14 | 28-Jul-14 | 49 |
| L15-8132 | L15 - Contractor Pre-Punchlist | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 50 |
| L15-8134 | L15 - Pre-Clean | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 47 |
| **Corridors / Common / Public Areas** | | | | | | |
| L15-8200 | L15 - Final Paint @ Common / Public Areas | 3 | 3 | 24-Jul-14 | 28-Jul-14 | 44 |
| L15-8202 | L15 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 29-Jul-14 | 31-Jul-14 | 44 |
| L15-8204 | L15 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 29-Jul-14 | 31-Jul-14 | 44 |
| L15-8206 | L15 - Flooring @ Common / Public Areas | 3 | 3 | 31-Jul-14 | 04-Aug-14 | 44 |
| L15-8208 | L15 - Final Clean | 3 | 3 | 05-Aug-14 | 07-Aug-14 | 44 |
| L15-8210 | L15 - Owner Walk / Create Punchlist | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 44 |
| L15-8212 | L15 - Final Punchlist | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 44 |
| L15-8214 | L15 - Floor Complete | 0 | 0 | | 15-Aug-14 | 44 |
| **Level 16 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L16-8100 | L16 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 29-May-14 | 02-Jun-14 | 53 |
| L16-6026 | L16 - Pull Wire | 6 | 6 | 29-May-14 | 05-Jun-14 | 76 |
| L16-8102 | L16 - GWB Hang / Tape / Finish - (Including Commor | 14 | 14 | 16-Jun-14 | 03-Jul-14 | 44 |
| L16-8104 | L16 - Int Painting | 5 | 5 | 01-Jul-14 | 08-Jul-14 | 44 |

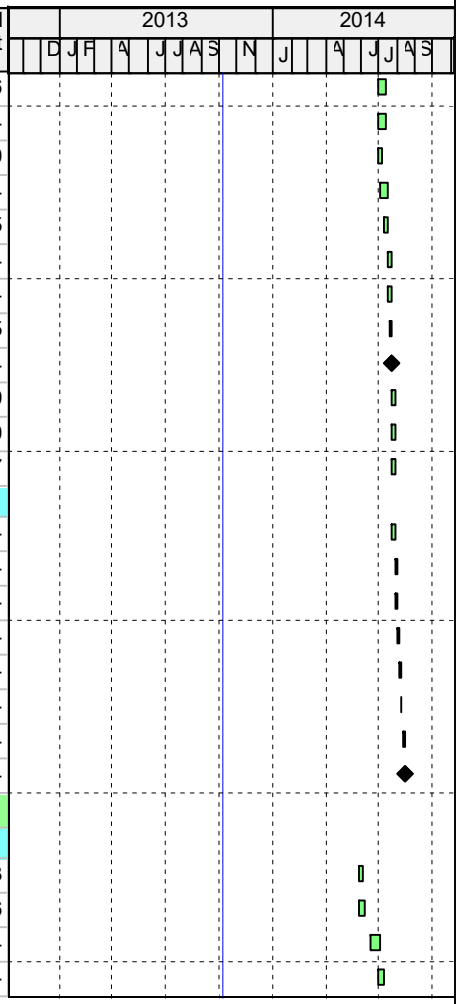



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8106 | L16 - Wallcoverings | 6 | 6 | 03-Jul-14 | 11-Jul-14 | 51 |
| L16-8108 | L16 - Elec Trim / Finish | 8 | 8 | 09-Jul-14 | 18-Jul-14 | 46 |
| L16-8110 | L16 - HVAC Trim / Finish | 8 | 8 | 09-Jul-14 | 18-Jul-14 | 46 |
| L16-8112 | L16 - Fire Sprinkler Trim / Finish | 8 | 8 | 09-Jul-14 | 18-Jul-14 | 46 |
| L16-8116 | L16 - Finish Carpentry / Millwork | 8 | 8 | 09-Jul-14 | 18-Jul-14 | 44 |
| L16-8118 | L16 - Elec Specialties Trim / Finish | 4 | 4 | 09-Jul-14 | 14-Jul-14 | 50 |
| L16-8120 | L16 - Ceramic Tile / Counter Tops | 8 | 8 | 11-Jul-14 | 22-Jul-14 | 44 |
| L16-8122 | L16 - Plumbing Trim / Finish | 8 | 8 | 15-Jul-14 | 24-Jul-14 | 45 |
| L16-8124 | L16 - Flooring @ Guest Rooms | 5 | 5 | 23-Jul-14 | 29-Jul-14 | 44 |
| L16-8126 | L16 - Doors & Hardware | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 44 |
| L16-8128 | L16 - Bath Specialties / Tub Glazing | 3 | 3 | 25-Jul-14 | 29-Jul-14 | 45 |
| L16-8130 | L16 - Guest Rooms Substantially Complete | 0 | 0 | | 30-Jul-14 | 44 |
| L16-8114 | L16 - Signage | 3 | 3 | 31-Jul-14 | 04-Aug-14 | 49 |
| L16-8132 | L16 - Contractor Pre-Punchlist | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 50 |
| L16-8134 | L16 - Pre-Clean | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 47 |
| **Corridors / Common / Public Areas** | | | | | | |
| L16-8200 | L16 - Final Paint @ Common / Public Areas | 3 | 3 | 31-Jul-14 | 04-Aug-14 | 44 |
| L16-8202 | L16 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 05-Aug-14 | 07-Aug-14 | 44 |
| L16-8204 | L16 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 05-Aug-14 | 07-Aug-14 | 44 |
| L16-8206 | L16 - Flooring @ Common / Public Areas | 3 | 3 | 07-Aug-14 | 11-Aug-14 | 44 |
| L16-8208 | L16 - Final Clean | 3 | 3 | 12-Aug-14 | 14-Aug-14 | 44 |
| L16-8210 | L16 - Owner Walk / Create Punchlist | 1 | 1 | 15-Aug-14 | 15-Aug-14 | 44 |
| L16-8212 | L16 - Final Punchlist | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 44 |
| L16-8214 | L16 - Floor Complete | 0 | 0 | | 22-Aug-14 | 44 |
| **Level 17 - (Guest Rooms)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L17-8100 | L17 - Insulation / Slab Edge Fire Proofing | 3 | 3 | 02-Jun-14 | 04-Jun-14 | 56 |

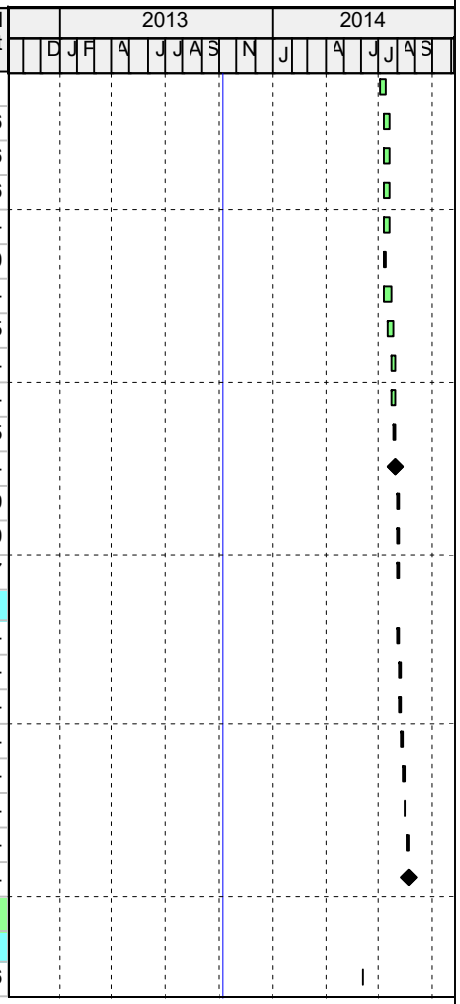



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6026 | L17 - Pull Wire | 6 | 6 | 02-Jun-14 | 09-Jun-14 | 79 |
| L17-8102 | L17 - GWB Hang / Tape / Finish - (Including Commor | 14 | 14 | 23-Jun-14 | 11-Jul-14 | 44 |
| L17-8104 | L17 - Int Painting | 5 | 5 | 09-Jul-14 | 15-Jul-14 | 44 |
| L17-8106 | L17 - Wallcoverings | 6 | 6 | 11-Jul-14 | 18-Jul-14 | 51 |
| L17-8108 | L17 - Elec Trim / Finish | 8 | 8 | 16-Jul-14 | 25-Jul-14 | 46 |
| L17-8110 | L17 - HVAC Trim / Finish | 8 | 8 | 16-Jul-14 | 25-Jul-14 | 46 |
| L17-8112 | L17 - Fire Sprinkler Trim / Finish | 8 | 8 | 16-Jul-14 | 25-Jul-14 | 46 |
| L17-8116 | L17 - Finish Carpentry / Millwork | 8 | 8 | 16-Jul-14 | 25-Jul-14 | 44 |
| L17-8118 | L17 - Elec Specialties Trim / Finish | 4 | 4 | 16-Jul-14 | 21-Jul-14 | 50 |
| L17-8120 | L17 - Ceramic Tile / Counter Tops | 8 | 8 | 18-Jul-14 | 29-Jul-14 | 44 |
| L17-8122 | L17 - Plumbing Trim / Finish | 8 | 8 | 22-Jul-14 | 31-Jul-14 | 45 |
| L17-8124 | L17 - Flooring @ Guest Rooms | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 44 |
| L17-8126 | L17 - Doors & Hardware | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 44 |
| L17-8128 | L17 - Bath Specialties / Tub Glazing | 3 | 3 | 01-Aug-14 | 05-Aug-14 | 45 |
| L17-8130 | L17 - Guest Rooms Substantially Complete | 0 | 0 | | 06-Aug-14 | 44 |
| L17-8114 | L17 - Signage | 3 | 3 | 07-Aug-14 | 11-Aug-14 | 49 |
| L17-8132 | L17 - Contractor Pre-Punchlist | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 50 |
| L17-8134 | L17 - Pre-Clean | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 47 |
| **Corridors / Common / Public Areas** | | | | | | |
| L17-8200 | L17 - Final Paint @ Common / Public Areas | 3 | 3 | 07-Aug-14 | 11-Aug-14 | 44 |
| L17-8202 | L17 - Elec Trim / Finish @ Common / Public Areas | 3 | 3 | 12-Aug-14 | 14-Aug-14 | 44 |
| L17-8204 | L17 - Mech Trim / Finish @ Common / Public Areas | 3 | 3 | 12-Aug-14 | 14-Aug-14 | 44 |
| L17-8206 | L17 - Flooring @ Common / Public Areas | 3 | 3 | 14-Aug-14 | 18-Aug-14 | 44 |
| L17-8208 | L17 - Final Clean | 3 | 3 | 19-Aug-14 | 21-Aug-14 | 44 |
| L17-8210 | L17 - Owner Walk / Create Punchlist | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 44 |
| L17-8212 | L17 - Final Punchlist | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 44 |
| L17-8214 | L17 - Floor Complete | 0 | 0 | | 29-Aug-14 | 44 |

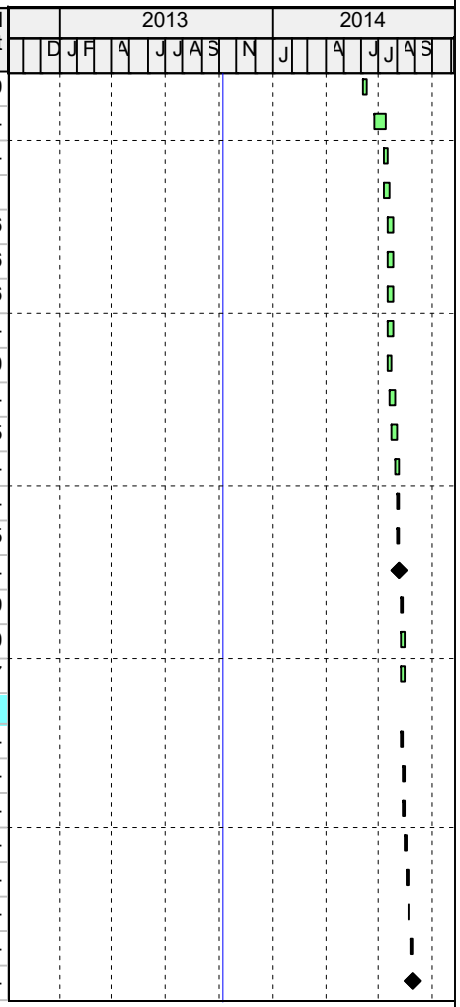



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Mech Penthouse** | | | | | | |
| PH-8100 | PH - Insulation | 3 | 3 | 13-Jun-14 | 17-Jun-14 | 58 |
| PH-6026 | PH - Pull Wire | 5 | 5 | 13-Jun-14 | 19-Jun-14 | 77 |
| PH-8102 | PH - GWB Hang / Tape / Finish - (Including Common | 10 | 10 | 23-Jun-14 | 07-Jul-14 | 55 |
| PH-8104 | PH - Int Painting | 4 | 4 | 02-Jul-14 | 08-Jul-14 | 55 |
| PH-8108 | PH - Elec Trim / Finish | 10 | 10 | 09-Jul-14 | 22-Jul-14 | 55 |
| PH-8110 | PH - HVAC Trim / Finish | 10 | 10 | 09-Jul-14 | 22-Jul-14 | 55 |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 5 | 5 | 09-Jul-14 | 15-Jul-14 | 60 |
| PH-8114 | PH - Signage | 2 | 2 | 09-Jul-14 | 10-Jul-14 | 71 |
| PH-8118 | PH - Elec Specialties Trim / Finish | 4 | 4 | 09-Jul-14 | 14-Jul-14 | 61 |
| PH-8116 | PH - Finish Carpentry / Millwork | 5 | 5 | 10-Jul-14 | 16-Jul-14 | 59 |
| PH-8122 | PH - Plumbing Trim / Finish | 5 | 5 | 16-Jul-14 | 22-Jul-14 | 60 |
| PH-8124 | PH - Flooring | 4 | 4 | 23-Jul-14 | 28-Jul-14 | 55 |
| PH-8126 | PH - Doors & Hardware | 3 | 3 | 25-Jul-14 | 29-Jul-14 | 55 |
| PH-8130 | PH - Guest Rooms Substantially Complete | 0 | 0 | | 29-Jul-14 | 55 |
| PH-8132 | PH - Contractor Pre-Punchlist | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 56 |
| PH-8134 | PH - Pre-Clean | 3 | 3 | 30-Jul-14 | 01-Aug-14 | 55 |
| PH-8208 | PH - Final Clean | 3 | 3 | 04-Aug-14 | 06-Aug-14 | 55 |
| PH-8210 | PH - Owner Walk / Create Punchlist | 1 | 1 | 07-Aug-14 | 07-Aug-14 | 55 |
| PH-8212 | PH - Final Punchlist | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 55 |
| PH-8214 | PH - Floor Complete | 0 | 0 | | 14-Aug-14 | 55 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| **Smoke Control** | | | | | | |
| CO-7104 | Smoke Control Pre-Testing | 10 | 10 | 02-Sep-14 | 15-Sep-14 | -25 |
| CO-7106 | City of Bellevue Smoke Control Testing | 5 | 5 | 16-Sep-14 | 22-Sep-14 | -25 |
| CO-7108 | Final Marriott Smoke Control Testing | 5 | 5 | 23-Sep-14 | 29-Sep-14 | -25 |
| **Fire Sprinklers** | | | | | | |

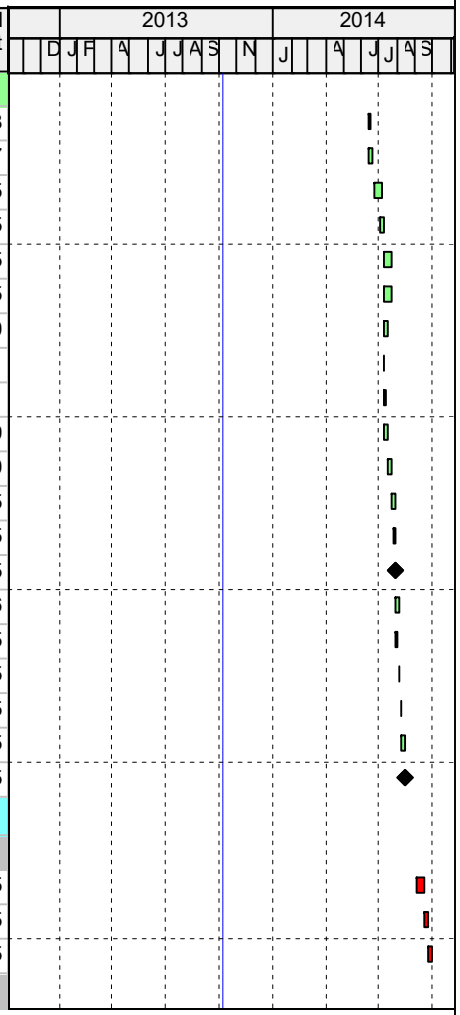



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7110 | Fire Sprinkler Pre-Testing | 10 | 10 | 02-Sep-14 | 15-Sep-14 | -25 |
| CO-7112 | City of Bellevue Fire Sprinkler Inspection / Approval | 5 | 5 | 16-Sep-14 | 22-Sep-14 | -25 |
| CO-7114 | Marriott Fire Sprinkler Testing | 5 | 5 | 23-Sep-14 | 29-Sep-14 | -25 |
| **Fire Alarm** | | | | | | |
| CO-7116 | Fire Alarm Pre-Testing | 10 | 10 | 02-Sep-14 | 15-Sep-14 | -25 |
| CO-7118 | City of Bellevue Fire Alarm Inspection / Approval | 5 | 5 | 16-Sep-14 | 22-Sep-14 | -25 |
| CO-7120 | Marriott Fire Alarm Testing | 5 | 5 | 23-Sep-14 | 29-Sep-14 | -25 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| CO-7100 | CO - Preliminary Start-Up & Testing | 20 | 20 | 04-Aug-14 | 29-Aug-14 | -25 |
| CO-7102 | CO - HVAC Commissioning | 2 | 2 | 02-Sep-14 | 03-Sep-14 | 19 |

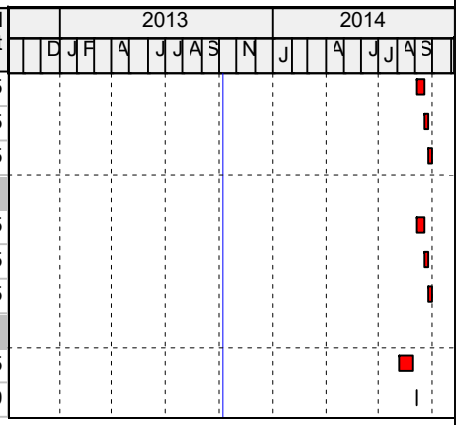



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Working Baseline Schedule 12-6-13 Update** | | | | | | |
| MM-1000 | MM - Temporary Power Available | 86 | 0 | 08-Jul-13 A | 08-Jul-13 A | |
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13 A | | |
| CM-1002 | CM - Contract Time (578 Cal Days) | 576 | 309 | 06-Mar-13 A | 05-Oct-14 | 1 |
| CM-1014 | CM - Start of Construction | 0 | 0 | 05-Apr-13 A | | |
| CM-1006 | Construction Documents Issued by Client - (Due on 7 | 0 | 0 | 01-Dec-13 | | 310 |
| CM-1008 | Finalization of Allowances - (Due on 9-2-13) | 0 | 0 | 01-Dec-13 | | 310 |
| CO-7004 | CO - Prep / Submit O&M Manuals | 40 | 40 | 01-Aug-14 | 09-Sep-14 | 27 |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 24-Aug-14* | | 0 |
| CM-1016 | CM - Owner FF+E "Build-Out" | 42 | 42 | 24-Aug-14* | 04-Oct-14 | 0 |
| CM-1018 | CM - Hotel Operations Training | 21 | 21 | 14-Sep-14* | 04-Oct-14 | 0 |
| CO-7006 | CO - Certificate of Occupancy/Substantial Completior | 0 | 0 | | 06-Oct-14 | 0 |
| CO-7122 | CO - Certificate of Occupancy | 0 | 0 | | 06-Oct-14 | 0 |
| **Misc Milestones** | | | | | | |
| CM-1020 | MM - Site Mobilization | 10 | 0 | 06-Mar-13 A | 04-Apr-13 A | |
| MM-1004 | MM - Start Drywall In Tower | 0 | 0 | 18-Mar-14 | | 203 |
| MM-1010 | MM - Permanent Power Available | 5 | 5 | 07-Apr-14 | 11-Apr-14 | 178 |
| MM-1008 | MM - Top Out - Tower / Structure | 0 | 0 | | 08-Apr-14 | 182 |
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 12-Aug-14 | 38 |
| **Executive Summary** | | | | | | |
| ES-1020 | Windows | 72 | 72 | 17-Feb-14 | 28-May-14 | 60 |
| ES-1010 | Elevators | 120 | 120 | 16-Apr-14 | 03-Oct-14 | 1 |
| ES-1016 | Metal Wall Panels @ Podium | 10 | 10 | 30-Apr-14 | 13-May-14 | 5 |

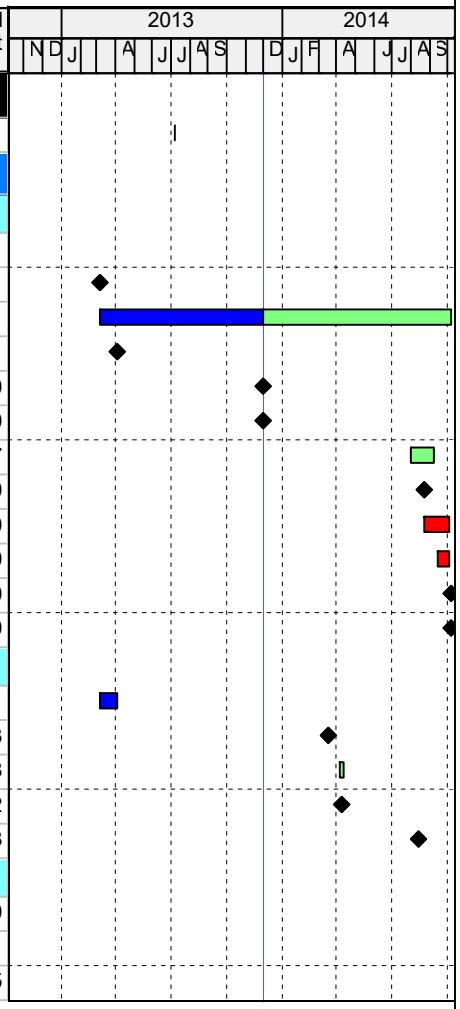


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ES-1018 | Curtainwall East | 10 | 10 | 15-Aug-14 | 28-Aug-14 | 0 |
| ES-1022 | Start-Up / Testing / Commissioning | 50 | 50 | 18-Aug-14 | 06-Oct-14 | 0 |
| ES-1024 | Curtainwall South | 10 | 10 | 02-Sep-14 | 15-Sep-14 | 15 |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| Tower Crane | | | | | | |
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 0 | 04-Jun-13 A | 14-Jun-13 A | |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 0 | 20-Jun-13 A | 24-Jun-13 A | |
| TC-5902 | Tower Crane - Erectiion | 2 | 0 | 21-Jun-13 A | 24-Jun-13 A | |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 24-Jun-13 A | | |
| TC-5906 | Tower Crane - Operatational Period | 391 | 207 | 24-Jun-13 A | 25-Jun-14 | 102 |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 1 | 26-Jun-14 | 26-Jun-14 | 70 |
| Man & Material Lifts | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 5 | 14-Jan-14 | 20-Jan-14 | 176 |
| ML-5952 | Man/Material Lifts - Erect/Build Loading Dock | 5 | 5 | 21-Jan-14 | 27-Jan-14 | 176 |
| ML-5954 | Man/Material Lifts - Load Test / Certify | 2 | 2 | 28-Jan-14 | 29-Jan-14 | 250 |
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 30-Jan-14 | | 250 |
| ML-5958 | Man/Material Lifts - Operatational Period | 207 | 207 | 30-Jan-14 | 24-Aug-14 | 22 |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 15 |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |
| Mass Excavation / Shoring | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 0 | 05-Apr-13 A | 12-Apr-13 A | |
| SW-2002 | Demolition And Utility Relocation | 8 | 0 | 15-Apr-13 A | 19-Apr-13 A | |
| SW-2010 | Grade Subgrade for Elect/Plumbing | 3 | 3 | 14-Jan-14 | 16-Jan-14 | 12 |
| Site Finishes | | | | | | |
| SW-2006 | Install Perm Power Electrical Service (Offsite) | 20 | 20 | 10-Feb-14 | 07-Mar-14 | 123 |

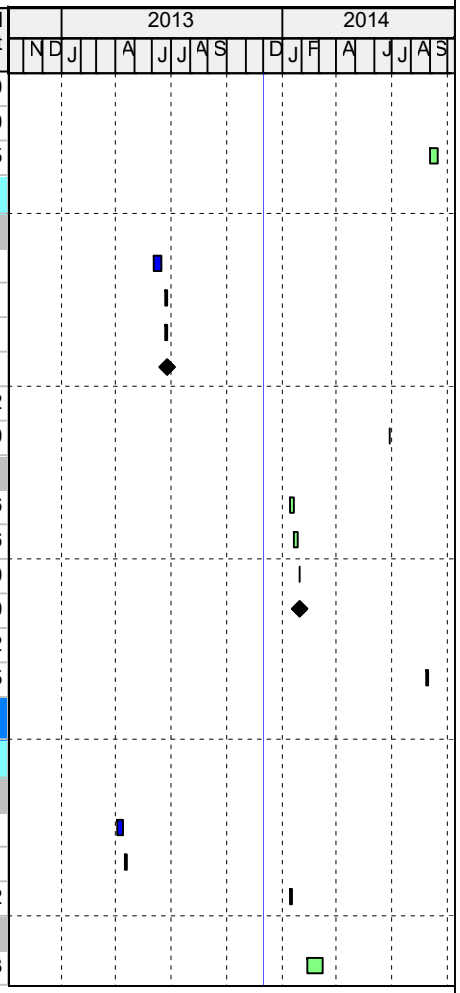



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2004 | Offsite Water & Water Connection | 20 | 20 | 24-Feb-14 | 21-Mar-14 | 138 |
| SW-2008 | Sidewalks / Landscaping / Street Improvements | 40 | 40 | 18-Jul-14 | 12-Sep-14 | 16 |
| **Structure** | | | | | | |
| **Foundation / Substructure - (Levels LL4 / LL3)** | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 0 | 12-Jun-13 A | 27-Jun-13 A | |
| LL4-1601 | LL4 - Excavate Footings | 14 | 0 | 17-Jun-13 A | 30-Jul-13 A | |
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 0 | 18-Jun-13 A | 24-Jun-13 A | |
| LL4-1606 | LL4 - Undrgrnd Plumbing | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-1608 | LL4 - Undrgrnd Elec | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 0 | 19-Jun-13 A | 25-Jun-13 A | |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 0 | 26-Jun-13 A | 02-Aug-13 A | |
| LL4-2033 | LL4 - Shotcrete Walls | 27 | 0 | 26-Jun-13 A | 05-Aug-13 A | |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 0 | 03-Jul-13 A | 21-Aug-13 A | |
| LL4-1614 | LL4 - FRP SOG | 5 | 0 | 10-Jul-13 A | 07-Aug-13 A | |
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 0 | 12-Jul-13 A | 26-Jul-13 A | |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 0 | 13-Jul-13 A | 06-Aug-13 A | |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 0 | 22-Jul-13 A | 24-Jul-13 A | |
| LL4-1618 | LL4 - FRP Ramp SOG | 5 | 0 | 01-Aug-13 A | 07-Aug-13 A | |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2004 | LL2 - Shore / Form Deck | 8 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2006 | LL3 - M & E Inserts | 4 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2008 | LL3 - ReSteel / PT Cables | 6 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2010 | LL3 - Install Embeds | 2 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2001 | LL3 - Waterproof Walls | 3 | 0 | 05-Aug-13 A | 05-Aug-13 A | |
| LL3-2012 | LL3 - Pour / Finish Deck | 2 | 0 | 16-Aug-13 A | 16-Aug-13 A | |
| LL3-2014 | LL3 - Stress Tendons | 1 | 0 | 19-Aug-13 A | 19-Aug-13 A | |

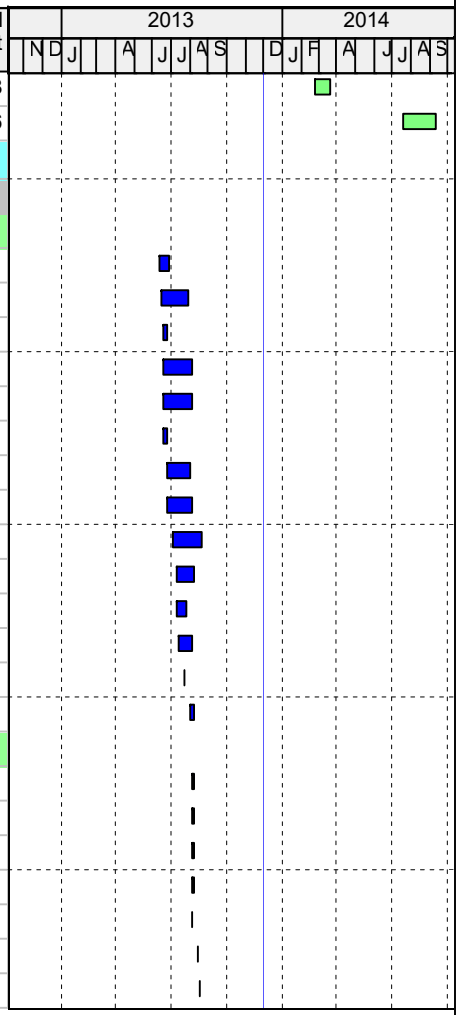


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-2000 | LL3 - FRP Core Walls | 8 | 0 | 19-Aug-13 A | 28-Aug-13 A | |
| LL3-2033 | LL3 - Shotcrete Walls | 5 | 0 | 23-Aug-13 A | 26-Aug-13 A | |
| LL3-2016 | LL3 - Strip / ReShore Deck | 3 | 0 | 01-Sep-13 A | 13-Sep-13 A | |
| LL3-2018 | LL3 - Remove ReShores | 4 | 0 | 04-Nov-13 A | 07-Nov-13 A | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Grids 1 to 4 - (SOG @ Loading Dock)** | | | | | | |
| LL2-2056 | LL2 - Grease Intercepter | 5 | 0 | 15-Aug-13 A | 21-Aug-13 A | |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 0 | 27-Aug-13 A | 04-Sep-13 A | |
| LL2-2027 | LL2 - Waterproof Walls | 2 | 0 | 27-Aug-13 A | 28-Aug-13 A | |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 0 | 30-Aug-13 A | 05-Sep-13 A | |
| LL2-2021 | LL2 - FRP Elec Vault | 14 | 0 | 30-Aug-13 A | 04-Sep-13 A | |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 0 | 04-Sep-13 A | 11-Sep-13 A | |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 0 | 11-Sep-13 A | 13-Sep-13 A | |
| LL2-2001 | LL2 - Excavation @ Loading Dock | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls/Roof | 11 | 0 | 19-Sep-13 A | 03-Oct-13 A | |
| LL2-2020 | LL2 - Undrgmd Plumbing | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2022 | LL2 - Undrgmd Elec | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2031 | LL2 - FRP Generator SOG | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2015 | LL2 to LL1 FRP Columns / Misc Walls | 6 | 0 | 01-Oct-13 A | 01-Oct-13 A | |
| LL2-2029 | LL2 - Ftgs & Foundations @ LL2 SOG | 8 | 8 | 23-Jan-14 | 03-Feb-14 | 12 |
| LL2-2011 | LL2 - FRP Loading Dock Ftgs / Fndtns | 5 | 5 | 04-Feb-14 | 10-Feb-14 | 12 |
| LL2-2024 | LL2 - Cap Fill / Fine Grade | 4 | 4 | 11-Feb-14 | 14-Feb-14 | 12 |
| LL2-2017 | LL2 - FRP Loading Dock Lwr & Upr SOG's | 8 | 8 | 17-Feb-14 | 26-Feb-14 | 12 |
| LL2-2019 | LL2 - FRP Loading Dock Stairs | 4 | 4 | 27-Feb-14 | 04-Mar-14 | 72 |
| LL2-2044 | LL2 - Set Generator | 1 | 1 | 27-Feb-14 | 27-Feb-14 | 12 |

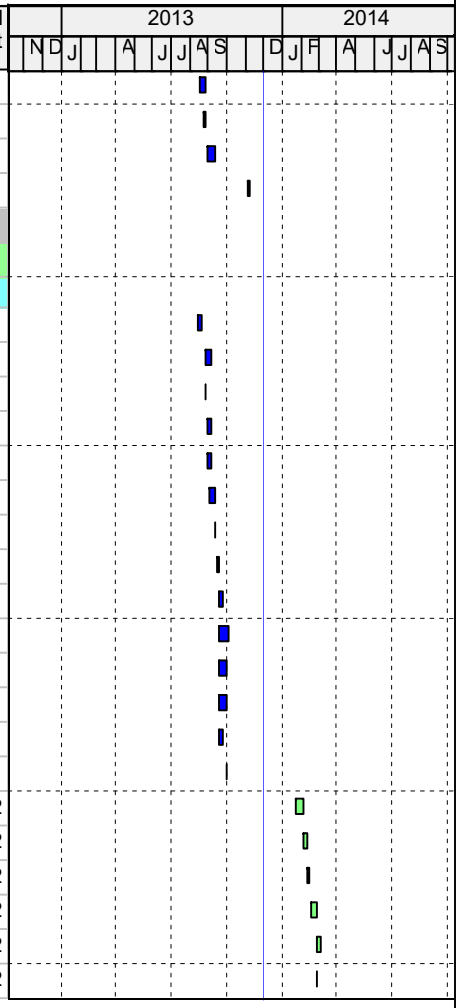



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |
| LL2-2004 | LL2 - Shore / Form Deck | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2035 | LL2 to LL1 - Shotcrete Walls | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2006 | LL2 - M & E Inserts | 4 | 0 | 14-Aug-13 A | 19-Aug-13 A | |
| LL2-2008 | LL2 - ReSteel / PT Cables | 6 | 0 | 14-Aug-13 A | 21-Aug-13 A | |
| LL2-2010 | LL2 - Install Embeds | 3 | 0 | 14-Aug-13 A | 16-Aug-13 A | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 0 | 27-Aug-13 A | 06-Sep-13 A | |
| LL2-2012 | LL2 - Place / Finish Deck | 3 | 0 | 29-Aug-13 A | 29-Aug-13 A | |
| LL2-2023 | LL2 - Waterproof Walls | 3 | 0 | 29-Aug-13 A | 03-Sep-13 A | |
| LL2-2014 | LL2 - Stress Tendons | 1 | 0 | 30-Aug-13 A | 30-Aug-13 A | |
| LL2-2016 | LL2 - Strip / ReShore | 3 | 0 | 03-Sep-13 A | 05-Sep-13 A | |
| LL2-8234 | LL2 - Place / Finish Deck | 3 | 0 | 12-Sep-13 A | 12-Sep-13 A | |
| LL2-2000 | LL2 - FRP Core Walls | 8 | 0 | 12-Sep-13 A | 23-Sep-13 A | |
| LL2-2018 | LL2 - Remove ReShores | 4 | 0 | 13-Nov-13 A | 18-Nov-13 A | |
| LL2-2013 | LL2 - Pour / Finish Ramp | 1 | 1 | 23-Jan-14 | 23-Jan-14 | 179 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| P5A-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2000 | LL1 - FRP Core Walls | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2004 | LL1 - Shore / Form Deck | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| P6-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P6-2004 | LL1 - Shore / Form Deck | 7 | 0 | 16-Sep-13 A | 24-Sep-13 A | |
| P5A-2006 | LL1 - MEP Rough In | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2008 | LL1 - ReSteel / PT Cables | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2012 | LL1 - Place / Finish Deck | 0 | 0 | 20-Sep-13 A | | |
| P5A-2020 | LL1 - Waterproof Walls | 3 | 0 | 20-Sep-13 A | 24-Sep-13 A | |
| P5A-2014 | LL1 - Stress Tendons | 1 | 0 | 23-Sep-13 A | 23-Sep-13 A | |

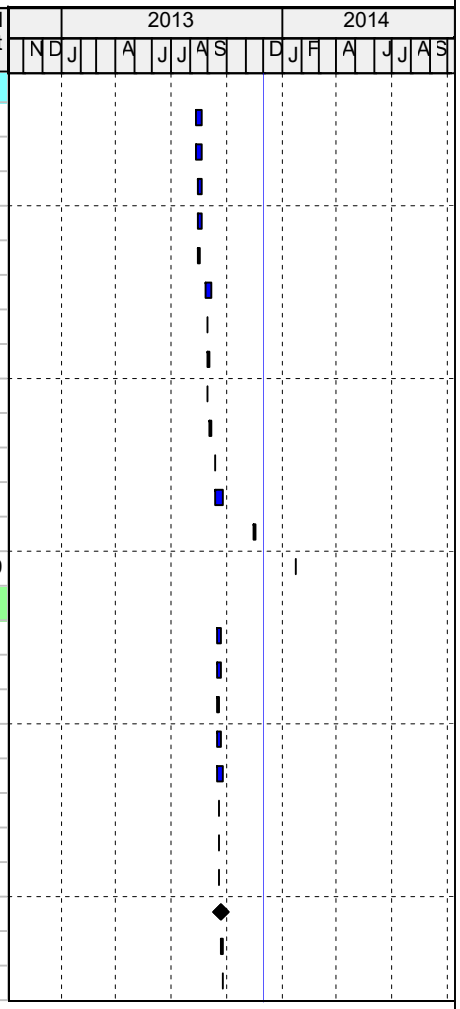



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P5A-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2006 | LL1 - MEP Rough In | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2008 | LL1 - ReSteel / PT Cables | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 24-Sep-13 A | 25-Sep-13 A | |
| P6-2020 | LL1 - Waterproof Walls | 4 | 0 | 24-Sep-13 A | 27-Sep-13 A | |
| P5A-2033 | LL1 - Resteel/Shotcrete Walls | 3 | 0 | 25-Sep-13 A | 27-Sep-13 A | |
| P5B-2002 | LL1 - FRP Columns Below | 5 | 0 | 26-Sep-13 A | 02-Oct-13 A | |
| P5B-2004 | LL1 - Shore / Form Deck | 7 | 0 | 26-Sep-13 A | 04-Oct-13 A | |
| P6-2012 | LL1 - Place / Finish Deck | 0 | 0 | 27-Sep-13 A | | |
| P6-2014 | LL1 - Stress Tendons | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2033 | LL1 - Resteel/Shotcrete Walls | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 01-Oct-13 A | 03-Oct-13 A | |
| P5B-2006 | LL1 - MEP Rough In | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2002 | FRP Columns Below | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2004 | Shore / Form Deck | 4 | 0 | 03-Oct-13 A | 08-Oct-13 A | |
| P5B-2008 | LL1 - ReSteel / PT Cables | 5 | 0 | 04-Oct-13 A | 10-Oct-13 A | |
| P5B-2010 | LL1 - Install Edgeform/Embeds | 4 | 0 | 04-Oct-13 A | 09-Oct-13 A | |
| P8-2002 | FRP Columns Below | 5 | 0 | 07-Oct-13 A | 11-Oct-13 A | |
| P8-2000 | Form/Resteel/Close Core Walls | 14 | 0 | 07-Oct-13 A | 24-Oct-13 A | |
| P8-2004 | Shore / Form Deck P8 | 8 | 0 | 07-Oct-13 A | 16-Oct-13 A | |
| P7-2002 | FRP Columns Below | 5 | 0 | 08-Oct-13 A | 14-Oct-13 A | |
| P7-2004 | Shore / Form Deck | 6 | 0 | 08-Oct-13 A | 15-Oct-13 A | |
| P10A--2006 | MEP Rough In | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2008 | ReSteel / PT Cables | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2010 | Install Edgeform/Embeds | 2 | 0 | 08-Oct-13 A | 09-Oct-13 A | |
| P5B-2012 | LL1 - Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P10A--2012 | Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |

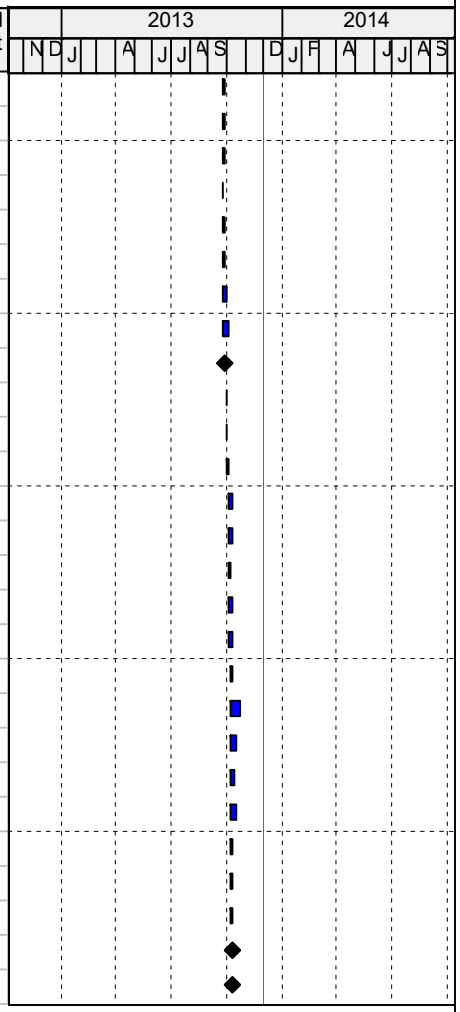



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P5B-2014 | LL1 - Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P7-2006 | MEP Rough In | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P7-2008 | ReSteel / PT Cables | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P10A--2014 | Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P8-2020 | Shore / Form Deck P9 | 6 | 0 | 14-Oct-13 A | 21-Oct-13 A | |
| P5B-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2010 | Install Edgeform/Embeds | 2 | 0 | 15-Oct-13 A | 16-Oct-13 A | |
| P8-2006 | MEP Rough In | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2008 | ReSteel / PT Cables | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2010 | Install Edgeform/Embeds | 4 | 0 | 15-Oct-13 A | 18-Oct-13 A | |
| P10A--2016 | Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2012 | Place / Finish Deck | 0 | 0 | 18-Oct-13 A | | |
| P7-2033 | Resteel/Shotcrete Walls | 3 | 0 | 18-Oct-13 A | 22-Oct-13 A | |
| P7-2014 | Stress Tendons | 1 | 0 | 21-Oct-13 A | 21-Oct-13 A | |
| P7-2016 | Strip / ReShore Deck | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2002 | FRP Columns Below | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P10B--2000 | FRP Shear Walls Below | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2004 | Shore / Form Deck | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P8-2012 | Place / Finish Deck P 8 & 9 and Core Walls | 0 | 0 | 25-Oct-13 A | | |
| P8-2014 | Stress Tendons | 1 | 0 | 28-Oct-13 A | 28-Oct-13 A | |
| P10B--2006 | MEP Rough In | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2008 | ReSteel / PT Cables | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2010 | Install Edgeform/Embeds | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P12--2002 | FRP Columns Below | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P12--2000 | Form/Resteel/Close Core Walls | 9 | 0 | 28-Oct-13 A | 07-Nov-13 A | |
| P12--2004 | Shore / Form Deck | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P8-2016 | Strip / ReShore Deck | 3 | 0 | 29-Oct-13 A | 31-Oct-13 A | |

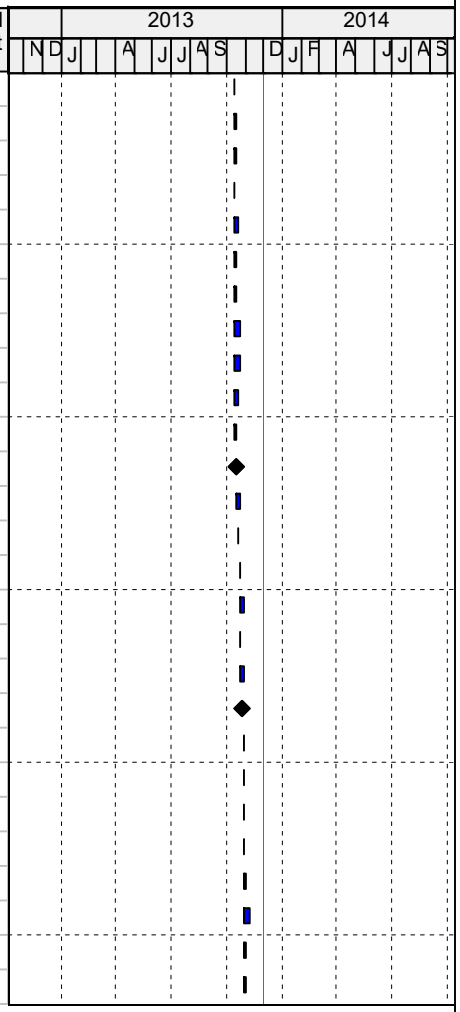



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P11–2002 | FRP Columns Below | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P11–2004 | Shore / Form Deck | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P10B–2012 | Place / Finish Deck | 0 | 0 | 31-Oct-13 A | | |
| P10B–2014 | Stress Tendons | 1 | 0 | 01-Nov-13 A | 01-Nov-13 A | |
| P12–2006 | MEP Rough In | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12–2008 | ReSteel / PT Cables | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12–2010 | Install Edgeform/Embeds | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P10B–2016 | Strip / ReShore Deck | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2006 | MEP Rough In | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2008 | ReSteel / PT Cables | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2010 | Install Edgeform/Embeds | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2012 | Place / Finish Deck | 0 | 0 | 07-Nov-13 A | | |
| P13–2002 | FRP Columns Below | 5 | 0 | 07-Nov-13 A | 14-Nov-13 A | |
| P13–2004 | Shore / Form Deck | 9 | 0 | 07-Nov-13 A | 28-Nov-13 A | |
| P11–2014 | Stress Tendons | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| P12–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 08-Nov-13 A | | |
| P11–2016 | Strip / ReShore Deck | 3 | 0 | 12-Nov-13 A | 14-Nov-13 A | |
| P12–2014 | Stress Tendons | 1 | 0 | 12-Nov-13 A | 12-Nov-13 A | |
| P12–2016 | Strip / ReShore Deck | 3 | 0 | 13-Nov-13 A | 15-Nov-13 A | |
| P14–2002 | FRP Columns Below | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P14–2000 | Form/Resteel/Close Core Walls | 8 | 2 | 19-Nov-13 A | 03-Dec-13 | 0 |
| P14–2004 | Shore / Form Deck | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P13A–2002 | FRP Columns Below | 5 | 0 | 21-Nov-13 A | 27-Nov-13 A | |
| P13A–2004 | Shore / Form Deck | 4 | 0 | 21-Nov-13 A | 26-Nov-13 A | |
| P13–2010 | Install Edgeform/Embeds | 5 | 0 | 22-Nov-13 A | 04-Dec-13 A | |
| P13–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2006 | MEP Rough In | 5 | 2 | 25-Nov-13 A | 03-Dec-13 | 0 |

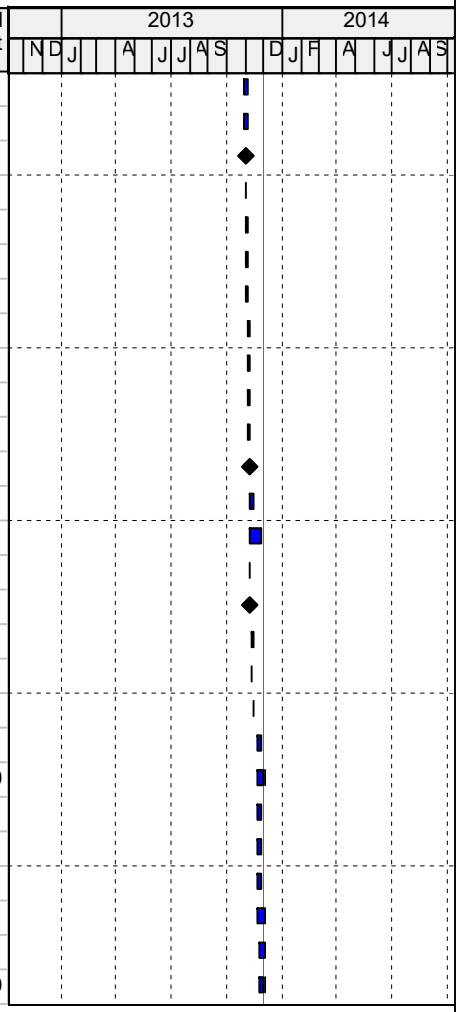



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P14–2008 | ReSteel / PT Cables | 5 | 2 | 25-Nov-13 A | 03-Dec-13 | 0 |
| P14–2010 | Install Edgeform/Embeds | 5 | 2 | 25-Nov-13 A | 03-Dec-13 | 0 |
| P13–2006 | MEP Rough In | 5 | 0 | 26-Nov-13 A | 03-Dec-13 A | |
| P13A–2006 | MEP Rough In | 3 | 1 | 26-Nov-13 A | 02-Dec-13 | 206 |
| P13A–2008 | ReSteel / PT Cables | 3 | 1 | 26-Nov-13 A | 02-Dec-13 | 206 |
| P13A–2010 | Install Edgeform/Embeds | 3 | 1 | 26-Nov-13 A | 02-Dec-13 | 206 |
| P13–2012 | Place / Finish Deck | 0 | 0 | 02-Dec-13* | | 205 |
| P13A–2012 | Place / Finish Deck | 0 | 0 | 03-Dec-13 | | 206 |
| P14–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 04-Dec-13 | | 0 |
| P13–2014 | Stress Tendons | 1 | 1 | 05-Dec-13 | 05-Dec-13 | 294 |
| P15–2002 | FRP Columns Below | 3 | 3 | 05-Dec-13 | 09-Dec-13 | 210 |
| P15–2000 | Jump/Resteel/Close Core | 9 | 9 | 05-Dec-13 | 17-Dec-13 | 204 |
| P15–2004 | Shore / Form Deck | 5 | 5 | 05-Dec-13 | 11-Dec-13 | 0 |
| P13–2016 | Strip / ReShore Deck | 3 | 3 | 06-Dec-13 | 10-Dec-13 | 205 |
| P13A–2014 | Stress Tendons | 1 | 1 | 06-Dec-13 | 06-Dec-13 | 297 |
| P14–2014 | Stress Tendons | 1 | 1 | 07-Dec-13 | 07-Dec-13 | 101 |
| P13A–2016 | Strip / ReShore Deck | 3 | 3 | 09-Dec-13 | 11-Dec-13 | 206 |
| P14–2016 | Strip / ReShore Deck | 3 | 3 | 09-Dec-13 | 11-Dec-13 | 70 |
| P15–2006 | MEP Rough In | 5 | 5 | 11-Dec-13 | 17-Dec-13 | 0 |
| P15–2008 | ReSteel / PT Cables | 5 | 5 | 11-Dec-13 | 17-Dec-13 | 0 |
| P15–2010 | Install Edgeform/Embeds | 3 | 3 | 11-Dec-13 | 13-Dec-13 | 2 |
| P16-2002 | FRP Columns Below | 5 | 5 | 16-Dec-13 | 20-Dec-13 | 201 |
| P16-2004 | Shore / Form Deck | 5 | 5 | 16-Dec-13 | 20-Dec-13 | 0 |
| P15–2012 | Place / Finish Deck | 0 | 0 | 18-Dec-13 | | 0 |
| P15–2020 | Place Conc @ Core | 0 | 0 | 18-Dec-13 | | 204 |
| P16-2000 | Jump/Resteel/Close Core | 5 | 5 | 18-Dec-13 | 24-Dec-13 | 199 |
| P16-2006 | MEP Rough In | 3 | 3 | 20-Dec-13 | 24-Dec-13 | 0 |

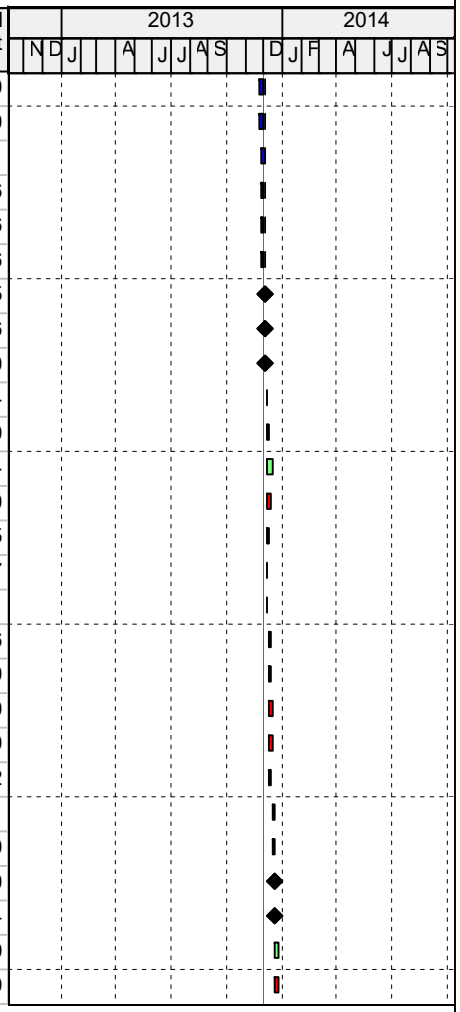


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P16-2008 | ReSteel / PT Cables | 3 | 3 | 20-Dec-13 | 24-Dec-13 | 0 |
| P16-2010 | Install Edgeform/Embeds | 3 | 3 | 20-Dec-13 | 24-Dec-13 | 0 |
| P15--2014 | Stress Tendons | 1 | 1 | 21-Dec-13 | 21-Dec-13 | 1 |
| P8-2018 | Remove Reshores | 2 | 2 | 23-Dec-13 | 24-Dec-13 | 0 |
| P15--2016 | Strip / ReShore Deck | 3 | 3 | 23-Dec-13 | 26-Dec-13 | 25 |
| P10A--2018 | Remove Reshores | 2 | 2 | 26-Dec-13 | 27-Dec-13 | 0 |
| P16-2012 | Place / Finish Deck | 0 | 0 | 26-Dec-13 | | 0 |
| P16-2020 | Place Conc @ Core | 0 | 0 | 26-Dec-13 | | 199 |
| P17-2002 | FRP Columns Below | 5 | 5 | 27-Dec-13 | 03-Jan-14 | 193 |
| P17-2000 | Jump/Resteel/Close Core | 7 | 7 | 27-Dec-13 | 07-Jan-14 | 191 |
| P17-2004 | Shore / Form Deck | 5 | 5 | 27-Dec-13 | 03-Jan-14 | 0 |
| P10B--2018 | Remove Reshores | 2 | 2 | 30-Dec-13 | 31-Dec-13 | 0 |
| P16-2014 | Stress Tendons | 1 | 1 | 31-Dec-13 | 31-Dec-13 | 19 |
| P5A-2018 | LL1 - Remove Reshores | 2 | 2 | 02-Jan-14 | 03-Jan-14 | 12 |
| P11--2018 | Remove Reshores | 2 | 2 | 02-Jan-14 | 03-Jan-14 | 193 |
| P12--2018 | Remove Reshores | 2 | 2 | 02-Jan-14 | 03-Jan-14 | 54 |
| P16-2016 | Strip / ReShore Deck | 3 | 3 | 02-Jan-14 | 06-Jan-14 | 24 |
| P17-2006 | MEP Rough In | 3 | 3 | 03-Jan-14 | 07-Jan-14 | 0 |
| P17-2008 | ReSteel / PT Cables | 3 | 3 | 03-Jan-14 | 07-Jan-14 | 0 |
| P17-2010 | Install Edgeform/Embeds | 3 | 3 | 03-Jan-14 | 07-Jan-14 | 0 |
| P6-2018 | LL1 - Remove Reshores | 2 | 2 | 06-Jan-14 | 07-Jan-14 | 12 |
| P5B-2018 | LL1 - Remove Reshores | 2 | 2 | 08-Jan-14 | 09-Jan-14 | 12 |
| P17-2012 | Place / Finish Deck | 0 | 0 | 08-Jan-14 | | 0 |
| P17-2020 | Place Conc @ Core | 0 | 0 | 08-Jan-14 | | 191 |
| P18-2002 | FRP Columns Below | 5 | 5 | 09-Jan-14 | 15-Jan-14 | 185 |
| P18-2000 | Jump/Resteel/Close Core | 4 | 4 | 09-Jan-14 | 14-Jan-14 | 186 |
| P18-2004 | Shore / Form Deck | 3 | 3 | 09-Jan-14 | 13-Jan-14 | 0 |

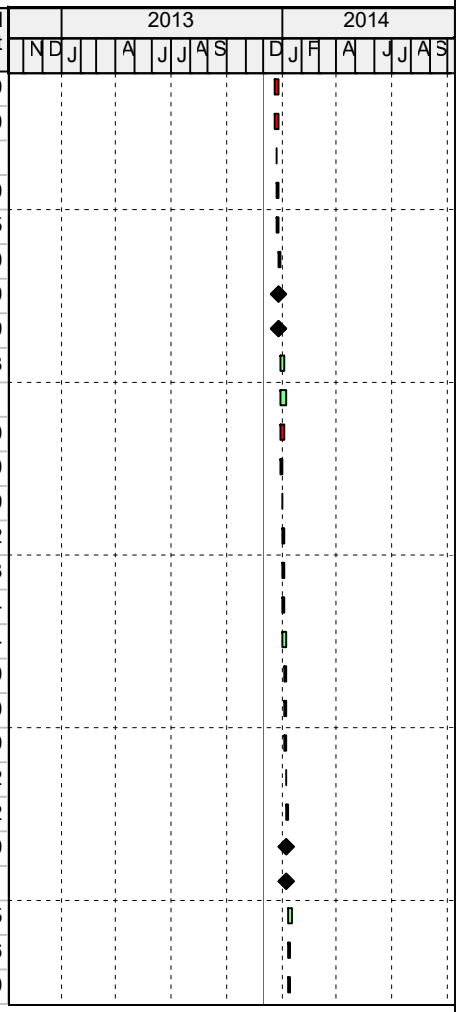


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P7-2018 | Remove Reshores | 2 | 2 | 10-Jan-14 | 13-Jan-14 | 12 |
| P17-2014 | Stress Tendons | 1 | 1 | 11-Jan-14 | 11-Jan-14 | 31 |
| P13--2018 | Remove Reshores | 2 | 2 | 13-Jan-14 | 14-Jan-14 | 184 |
| P17-2016 | Strip / ReShore Deck | 3 | 3 | 13-Jan-14 | 15-Jan-14 | 22 |
| P18-2006 | MEP Rough In | 2 | 2 | 13-Jan-14 | 14-Jan-14 | 0 |
| P18-2008 | ReSteel / PT Cables | 2 | 2 | 13-Jan-14 | 14-Jan-14 | 0 |
| P18-2010 | Install Edgeform/Embeds | 2 | 2 | 13-Jan-14 | 14-Jan-14 | 0 |
| P13A--2018 | Remove Reshores | 2 | 2 | 15-Jan-14 | 16-Jan-14 | 184 |
| P18-2012 | Place / Finish Deck | 0 | 0 | 15-Jan-14 | | 0 |
| P18-2020 | Place Conc @ Core | 0 | 0 | 15-Jan-14 | | 186 |
| P19-2002 | FRP Columns Below | 5 | 5 | 16-Jan-14 | 22-Jan-14 | 180 |
| P19-2000 | Jump/Resteel/Close Core | 4 | 4 | 16-Jan-14 | 21-Jan-14 | 181 |
| P19-2004 | Shore / Form Deck | 3 | 3 | 16-Jan-14 | 20-Jan-14 | 0 |
| LL2-2022R | MEP Rough In | 4 | 4 | 17-Jan-14 | 22-Jan-14 | 12 |
| P18-2014 | Stress Tendons | 1 | 1 | 18-Jan-14 | 18-Jan-14 | 13 |
| P14--2018 | Remove Reshores | 2 | 2 | 20-Jan-14 | 21-Jan-14 | 45 |
| P18-2016 | Strip / ReShore Deck | 3 | 3 | 20-Jan-14 | 22-Jan-14 | 22 |
| P19-2006 | MEP Rough In | 2 | 2 | 20-Jan-14 | 21-Jan-14 | 0 |
| P19-2008 | ReSteel / PT Cables | 2 | 2 | 20-Jan-14 | 21-Jan-14 | 0 |
| P19-2010 | Install Edgeform/Embeds | 2 | 2 | 20-Jan-14 | 21-Jan-14 | 0 |
| P19-2012 | Place / Finish Deck | 0 | 0 | 22-Jan-14 | | 0 |
| P19-2020 | Place Conc @ Core | 0 | 0 | 22-Jan-14 | | 181 |
| P20-2002 | FRP Columns Below | 5 | 5 | 23-Jan-14 | 29-Jan-14 | 175 |
| P20-2000 | Jump/Resteel/Close Core | 4 | 4 | 23-Jan-14 | 28-Jan-14 | 176 |
| P20-2004 | Shore / Form Deck | 3 | 3 | 23-Jan-14 | 27-Jan-14 | 0 |
| P19-2014 | Stress Tendons | 1 | 1 | 25-Jan-14 | 25-Jan-14 | 8 |
| L03-2018 | Remove Reshores | 2 | 2 | 27-Jan-14 | 28-Jan-14 | 5 |

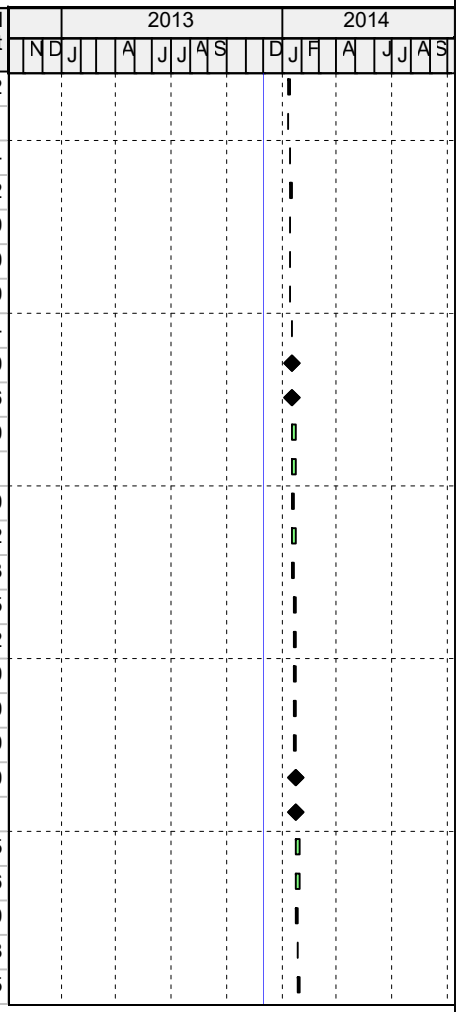



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P19-2016 | Strip / ReShore Deck | 3 | 3 | 27-Jan-14 | 29-Jan-14 | 22 |
| P20-2006 | MEP Rough In | 2 | 2 | 27-Jan-14 | 28-Jan-14 | 0 |
| P20-2008 | ReSteel / PT Cables | 2 | 2 | 27-Jan-14 | 28-Jan-14 | 0 |
| P20-2010 | Install Edgeform/Embeds | 2 | 2 | 27-Jan-14 | 28-Jan-14 | 0 |
| P20-2012 | Place / Finish Deck | 0 | 0 | 29-Jan-14 | | 0 |
| P20-2020 | Place Conc @ Core | 0 | 0 | 29-Jan-14 | | 176 |
| L03-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 29-Jan-14 | 04-Feb-14 | 5 |
| P21-2002 | FRP Columns Below | 5 | 5 | 30-Jan-14 | 05-Feb-14 | 170 |
| P21-2000 | Jump/Resteel/Close Core | 4 | 4 | 30-Jan-14 | 04-Feb-14 | 171 |
| P21-2004 | Shore / Form Deck | 3 | 3 | 30-Jan-14 | 03-Feb-14 | 0 |
| P20-2014 | Stress Tendons | 1 | 1 | 01-Feb-14 | 01-Feb-14 | 8 |
| P20-2016 | Strip / ReShore Deck | 3 | 3 | 03-Feb-14 | 05-Feb-14 | 22 |
| P21-2006 | MEP Rough In | 2 | 2 | 03-Feb-14 | 04-Feb-14 | 0 |
| P21-2008 | ReSteel / PT Cables | 2 | 2 | 03-Feb-14 | 04-Feb-14 | 0 |
| P21-2010 | Install Edgeform/Embeds | 2 | 2 | 03-Feb-14 | 04-Feb-14 | 0 |
| L04-2018 | Remove Reshores | 2 | 2 | 03-Feb-14 | 04-Feb-14 | 5 |
| P21-2012 | Place / Finish Deck | 0 | 0 | 05-Feb-14 | | 0 |
| P21-2020 | Place Conc @ Core | 0 | 0 | 05-Feb-14 | | 171 |
| L04-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 05-Feb-14 | 11-Feb-14 | 5 |
| P22-2002 | FRP Columns Below | 5 | 5 | 06-Feb-14 | 12-Feb-14 | 165 |
| P22-2000 | Jump/Resteel/Close Core | 4 | 4 | 06-Feb-14 | 11-Feb-14 | 166 |
| P22-2004 | Shore / Form Deck | 3 | 3 | 06-Feb-14 | 10-Feb-14 | 0 |
| P21-2014 | Stress Tendons | 1 | 1 | 08-Feb-14 | 08-Feb-14 | 8 |
| P21-2016 | Strip / ReShore Deck | 3 | 3 | 10-Feb-14 | 12-Feb-14 | 22 |
| P22-2006 | MEP Rough In | 2 | 2 | 10-Feb-14 | 11-Feb-14 | 0 |
| P22-2008 | ReSteel / PT Cables | 2 | 2 | 10-Feb-14 | 11-Feb-14 | 0 |
| P22-2010 | Install Edgeform/Embeds | 2 | 2 | 10-Feb-14 | 11-Feb-14 | 0 |

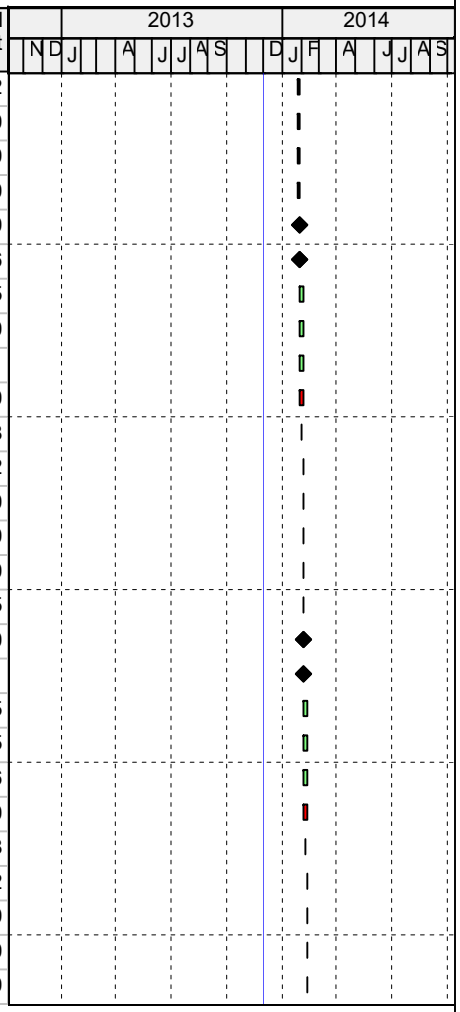



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-2018 | Remove Reshores | 2 | 2 | 10-Feb-14 | 11-Feb-14 | 5 |
| P22-2012 | Place / Finish Deck | 0 | 0 | 12-Feb-14 | | 0 |
| P22-2020 | Place Conc @ Core | 0 | 0 | 12-Feb-14 | | 166 |
| L05-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 12-Feb-14 | 18-Feb-14 | 5 |
| P23-2002 | FRP Columns Below | 5 | 5 | 13-Feb-14 | 19-Feb-14 | 160 |
| P23-2000 | Jump/Resteel/Close Core | 4 | 4 | 13-Feb-14 | 18-Feb-14 | 161 |
| P23-2004 | Shore / Form Deck | 3 | 3 | 13-Feb-14 | 17-Feb-14 | 0 |
| P22-2014 | Stress Tendons | 1 | 1 | 15-Feb-14 | 15-Feb-14 | 8 |
| P22-2016 | Strip / ReShore Deck | 3 | 3 | 17-Feb-14 | 19-Feb-14 | 22 |
| P23-2006 | MEP Rough In | 2 | 2 | 17-Feb-14 | 18-Feb-14 | 0 |
| P23-2008 | ReSteel / PT Cables | 2 | 2 | 17-Feb-14 | 18-Feb-14 | 0 |
| P23-2010 | Install Edgeform/Embeds | 2 | 2 | 17-Feb-14 | 18-Feb-14 | 0 |
| L06-2018 | Remove Reshores | 2 | 2 | 17-Feb-14 | 18-Feb-14 | 5 |
| P23-2012 | Place / Finish Deck | 0 | 0 | 19-Feb-14 | | 0 |
| P23-2020 | Place Conc @ Core | 0 | 0 | 19-Feb-14 | | 161 |
| L06-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 19-Feb-14 | 25-Feb-14 | 5 |
| P24-2002 | FRP Columns Below | 5 | 5 | 20-Feb-14 | 26-Feb-14 | 155 |
| P24-2000 | Jump/Resteel/Close Core | 4 | 4 | 20-Feb-14 | 25-Feb-14 | 156 |
| P24-2004 | Shore / Form Deck | 3 | 3 | 20-Feb-14 | 24-Feb-14 | 0 |
| P23-2014 | Stress Tendons | 1 | 1 | 22-Feb-14 | 22-Feb-14 | 8 |
| P23-2016 | Strip / ReShore Deck | 3 | 3 | 24-Feb-14 | 26-Feb-14 | 22 |
| P24-2006 | MEP Rough In | 2 | 2 | 24-Feb-14 | 25-Feb-14 | 0 |
| P24-2008 | ReSteel / PT Cables | 2 | 2 | 24-Feb-14 | 25-Feb-14 | 0 |
| P24-2010 | Install Edgeform/Embeds | 2 | 2 | 24-Feb-14 | 25-Feb-14 | 0 |
| L07-2018 | Remove Reshores | 2 | 2 | 24-Feb-14 | 25-Feb-14 | 5 |
| P24-2012 | Place / Finish Deck | 0 | 0 | 26-Feb-14 | | 0 |
| P24-2020 | Place Conc @ Core | 0 | 0 | 26-Feb-14 | | 156 |

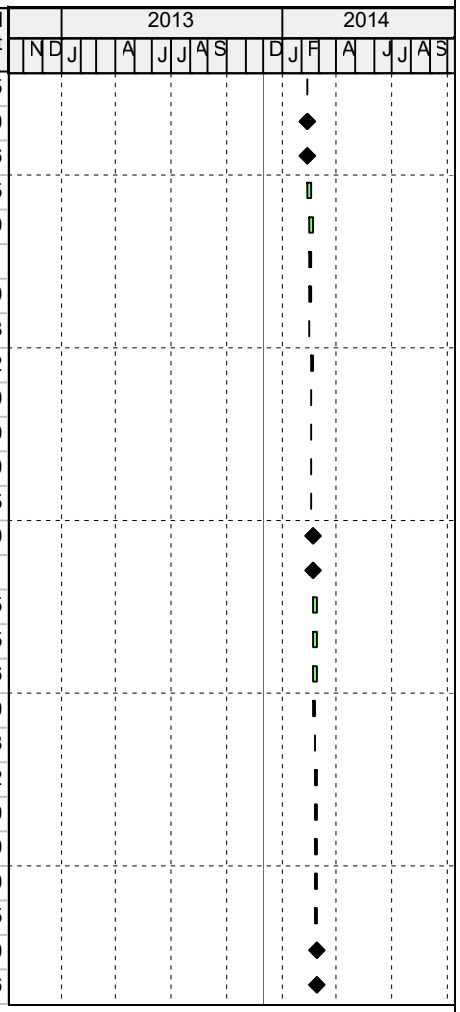



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 26-Feb-14 | 04-Mar-14 | 5 |
| P25-2002 | FRP Columns Below | 5 | 5 | 27-Feb-14 | 05-Mar-14 | 150 |
| P25-2000 | Jump/Resteel/Close Core | 4 | 4 | 27-Feb-14 | 04-Mar-14 | 151 |
| P25-2004 | Shore / Form Deck | 3 | 3 | 27-Feb-14 | 03-Mar-14 | 0 |
| P24-2014 | Stress Tendons | 1 | 1 | 01-Mar-14 | 01-Mar-14 | 8 |
| P24-2016 | Strip / ReShore Deck | 3 | 3 | 03-Mar-14 | 05-Mar-14 | 22 |
| P25-2006 | MEP Rough In | 2 | 2 | 03-Mar-14 | 04-Mar-14 | 0 |
| P25-2008 | ReSteel / PT Cables | 2 | 2 | 03-Mar-14 | 04-Mar-14 | 0 |
| P25-2010 | Install Edgeform/Embeds | 2 | 2 | 03-Mar-14 | 04-Mar-14 | 0 |
| L08-2018 | Remove Reshores | 2 | 2 | 03-Mar-14 | 04-Mar-14 | 5 |
| P25-2012 | Place / Finish Deck | 0 | 0 | 05-Mar-14 | | 0 |
| P25-2020 | Place Conc @ Core | 0 | 0 | 05-Mar-14 | | 151 |
| L08-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 05-Mar-14 | 11-Mar-14 | 5 |
| P26-2002 | FRP Columns Below | 5 | 5 | 06-Mar-14 | 12-Mar-14 | 145 |
| P26-2000 | Jump/Resteel/Close Core | 4 | 4 | 06-Mar-14 | 11-Mar-14 | 146 |
| P26-2004 | Shore / Form Deck | 3 | 3 | 06-Mar-14 | 10-Mar-14 | 0 |
| P25-2014 | Stress Tendons | 1 | 1 | 08-Mar-14 | 08-Mar-14 | 8 |
| P26-2006 | MEP Rough In | 2 | 2 | 10-Mar-14 | 11-Mar-14 | 0 |
| P26-2008 | ReSteel / PT Cables | 2 | 2 | 10-Mar-14 | 11-Mar-14 | 0 |
| P26-2010 | Install Edgeform/Embeds | 2 | 2 | 10-Mar-14 | 11-Mar-14 | 0 |
| P25-2016 | Strip / ReShore Deck | 3 | 3 | 10-Mar-14 | 12-Mar-14 | 22 |
| L09-2018 | Remove Reshores | 2 | 2 | 10-Mar-14 | 11-Mar-14 | 5 |
| P26-2012 | Place / Finish Deck | 0 | 0 | 12-Mar-14 | | 0 |
| P26-2020 | Place Conc @ Core | 0 | 0 | 12-Mar-14 | | 146 |
| L09-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 12-Mar-14 | 18-Mar-14 | 5 |
| P27-2002 | FRP Columns Below | 5 | 5 | 13-Mar-14 | 19-Mar-14 | 140 |
| P27-2000 | Jump/Resteel/Close Core | 4 | 4 | 13-Mar-14 | 18-Mar-14 | 141 |

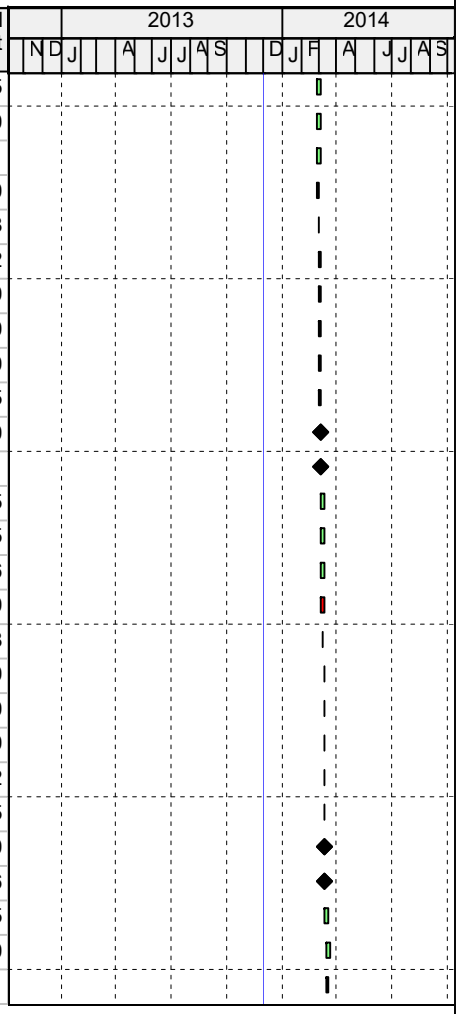



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P27-2004 | Shore / Form Deck | 3 | 3 | 13-Mar-14 | 17-Mar-14 | 0 |
| P26-2014 | Stress Tendons | 1 | 1 | 15-Mar-14 | 15-Mar-14 | 8 |
| P27-2006 | MEP Rough In | 2 | 2 | 17-Mar-14 | 18-Mar-14 | 0 |
| P27-2008 | ReSteel / PT Cables | 2 | 2 | 17-Mar-14 | 18-Mar-14 | 0 |
| P27-2010 | Install Edgeform/Embeds | 2 | 2 | 17-Mar-14 | 18-Mar-14 | 0 |
| P26-2016 | Strip / ReShore Deck | 3 | 3 | 17-Mar-14 | 19-Mar-14 | 22 |
| L10-2018 | Remove Reshores | 2 | 2 | 17-Mar-14 | 18-Mar-14 | 5 |
| P27-2012 | Place / Finish Deck | 0 | 0 | 19-Mar-14 | | 0 |
| P27-2020 | Place Conc @ Core | 0 | 0 | 19-Mar-14 | | 141 |
| L10-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 19-Mar-14 | 25-Mar-14 | 5 |
| P28-2002 | FRP Columns Below | 5 | 5 | 20-Mar-14 | 26-Mar-14 | 135 |
| P28-2000 | Jump/Resteel/Close Core | 9 | 9 | 20-Mar-14 | 01-Apr-14 | 1 |
| P28-2004 | Shore / Form Deck | 6 | 6 | 20-Mar-14 | 27-Mar-14 | 0 |
| P27-2014 | Stress Tendons | 1 | 1 | 22-Mar-14 | 22-Mar-14 | 8 |
| P27-2016 | Strip / ReShore Deck | 3 | 3 | 24-Mar-14 | 26-Mar-14 | 22 |
| L11-2018 | Remove Reshores | 2 | 2 | 24-Mar-14 | 25-Mar-14 | 5 |
| L11-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 26-Mar-14 | 01-Apr-14 | 5 |
| P28-2006 | MEP Rough In | 4 | 4 | 27-Mar-14 | 01-Apr-14 | 0 |
| P28-2008 | ReSteel / PT Cables | 4 | 4 | 27-Mar-14 | 01-Apr-14 | 0 |
| P28-2010 | Install Edgeform/Embeds | 2 | 2 | 27-Mar-14 | 28-Mar-14 | 2 |
| P28-2012 | Place / Finish Deck | 0 | 0 | 02-Apr-14 | | 0 |
| P28-2020 | Place Conc @ Core | 0 | 0 | 02-Apr-14 | | 1 |
| P29-2000 | Strip Core | 2 | 2 | 02-Apr-14 | 03-Apr-14 | 1 |
| P29-2002 | FRP Columns Above Roof Deck | 3 | 3 | 04-Apr-14 | 08-Apr-14 | 126 |
| P29-2004 | Shore / Form Deck | 2 | 2 | 04-Apr-14 | 07-Apr-14 | 1 |
| P28-2014 | Stress Tendons | 1 | 1 | 05-Apr-14 | 05-Apr-14 | 1 |
| P28-2016 | Strip / ReShore Deck | 3 | 3 | 07-Apr-14 | 09-Apr-14 | 17 |

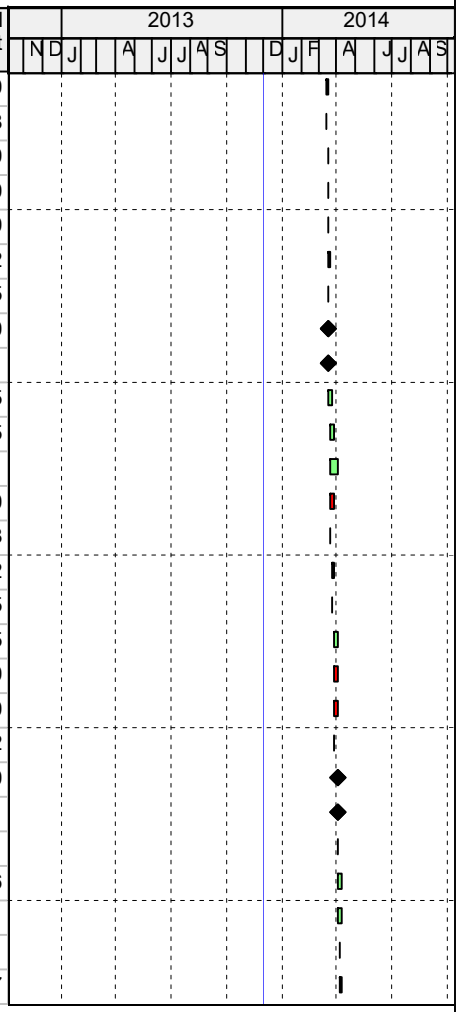



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P29-2006 | MEP Rough In | 1 | 1 | 07-Apr-14 | 07-Apr-14 | 1 |
| P29-2008 | ReSteel | 1 | 1 | 07-Apr-14 | 07-Apr-14 | 1 |
| P29-2010 | Install Edgeform/Embeds | 1 | 1 | 07-Apr-14 | 07-Apr-14 | 1 |
| L12-2018 | Remove Reshores | 2 | 2 | 07-Apr-14 | 08-Apr-14 | 0 |
| L14-2018 | Remove Reshores | 2 | 2 | 07-Apr-14 | 08-Apr-14 | 5 |
| P29-2012 | Place / Finish Deck | 0 | 0 | 08-Apr-14 | | 1 |
| L12-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 09-Apr-14 | 15-Apr-14 | 0 |
| L14-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 09-Apr-14 | 15-Apr-14 | 5 |
| L15-2018 | Remove Reshores | 2 | 2 | 09-Apr-14 | 10-Apr-14 | 8 |
| L15-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 11-Apr-14 | 17-Apr-14 | 8 |
| L16-2018 | Remove Reshores | 2 | 2 | 11-Apr-14 | 14-Apr-14 | 11 |
| L16-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 15-Apr-14 | 21-Apr-14 | 11 |
| L17-2018 | Remove Reshores | 2 | 2 | 15-Apr-14 | 16-Apr-14 | 14 |
| L17-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 17-Apr-14 | 23-Apr-14 | 14 |
| **Ballroom Catwalk & Roof** | | | | | | |
| PC-2100 | Erect Structural Steel @ Porte Cochere | 3 | 3 | 29-Jan-14 | 31-Jan-14 | 9 |
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 10 | 10 | 03-Feb-14 | 14-Feb-14 | 9 |
| PC-2102 | Metal Decking @ Ballroom Catwalk / Roof | 2 | 2 | 03-Feb-14 | 04-Feb-14 | 30 |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 3 | 17-Feb-14 | 19-Feb-14 | 9 |
| BR-2112 | BR - Fireproofing @ Structural Steel | 5 | 5 | 06-Mar-14 | 12-Mar-14 | 20 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Mech Penthouse** | | | | | | |
| PH-8702 | PH - Structural Steel / Decking / Framing | 10 | 10 | 15-Apr-14 | 28-Apr-14 | 1 |
| PH-8706 | Set Mech Equipment @ Tower Roof | 2 | 2 | 29-Apr-14 | 30-Apr-14 | 109 |
| PH-8708 | Set Equipment @ Penthouse | 3 | 3 | 29-Apr-14 | 01-May-14 | 70 |
| PH-8700 | High Roof - Structural Steel | 10 | 10 | 02-May-14 | 15-May-14 | 70 |
| **Vertical Circulation** | | | | | | |

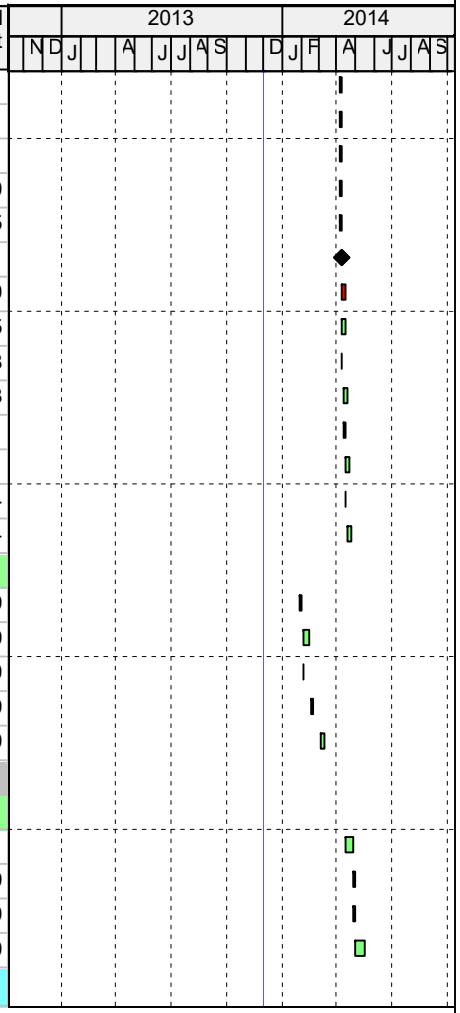



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Stairs** | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 25-Nov-13 A | 26-Nov-13 A | |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 2 | 2 | 27-Nov-13 A | 03-Dec-13 | 161 |
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 2 | 2 | 04-Dec-13 | 05-Dec-13 | 161 |
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 2 | 2 | 06-Dec-13 | 09-Dec-13 | 161 |
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 2 | 2 | 22-Jan-14 | 23-Jan-14 | 133 |
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 2 | 2 | 24-Jan-14 | 27-Jan-14 | 133 |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 2 | 2 | 28-Jan-14 | 29-Jan-14 | 133 |
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 2 | 2 | 30-Jan-14 | 31-Jan-14 | 133 |
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 2 | 2 | 26-Feb-14 | 27-Feb-14 | 116 |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 2 | 2 | 28-Feb-14 | 03-Mar-14 | 116 |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 2 | 2 | 04-Mar-14 | 05-Mar-14 | 116 |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 2 | 2 | 06-Mar-14 | 07-Mar-14 | 116 |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 2 | 2 | 02-Apr-14 | 03-Apr-14 | 99 |
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 2 | 2 | 04-Apr-14 | 07-Apr-14 | 99 |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 2 | 2 | 08-Apr-14 | 09-Apr-14 | 99 |
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 2 | 2 | 10-Apr-14 | 11-Apr-14 | 99 |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 2 | 2 | 14-Apr-14 | 15-Apr-14 | 107 |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 2 | 2 | 28-Apr-14 | 29-Apr-14 | 99 |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 2 | 2 | 30-Apr-14 | 01-May-14 | 99 |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 2 | 2 | 02-May-14 | 05-May-14 | 99 |
| S1-4040 | Stair 1 - Set Mtl Stairs / Railings L18 | 2 | 2 | 06-May-14 | 07-May-14 | 99 |
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 2 | 2 | 10-Dec-13 | 11-Dec-13 | 161 |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 2 | 2 | 12-Dec-13 | 13-Dec-13 | 161 |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 2 | 2 | 16-Dec-13 | 17-Dec-13 | 161 |

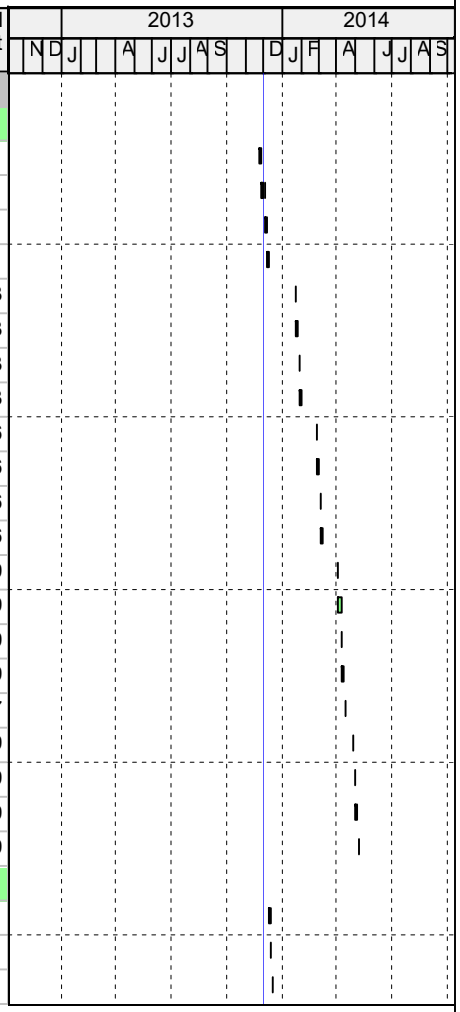



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 2 | 2 | 18-Dec-13 | 19-Dec-13 | 161 |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 2 | 2 | 03-Feb-14 | 04-Feb-14 | 133 |
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 2 | 2 | 05-Feb-14 | 06-Feb-14 | 133 |
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 2 | 2 | 07-Feb-14 | 10-Feb-14 | 133 |
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 2 | 2 | 11-Feb-14 | 12-Feb-14 | 133 |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 2 | 2 | 10-Mar-14 | 11-Mar-14 | 116 |
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 2 | 2 | 12-Mar-14 | 13-Mar-14 | 116 |
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 2 | 2 | 14-Mar-14 | 17-Mar-14 | 116 |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 2 | 2 | 18-Mar-14 | 19-Mar-14 | 116 |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 2 | 2 | 14-Apr-14 | 15-Apr-14 | 99 |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 2 | 2 | 16-Apr-14 | 17-Apr-14 | 99 |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 2 | 2 | 18-Apr-14 | 21-Apr-14 | 99 |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 2 | 2 | 22-Apr-14 | 23-Apr-14 | 99 |
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 2 | 2 | 24-Apr-14 | 25-Apr-14 | 99 |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 2 | 2 | 08-May-14 | 09-May-14 | 99 |
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 2 | 2 | 12-May-14 | 13-May-14 | 99 |
| S2-4038 | Stair 2 - Set Mtl Stairs / Railings L17 | 2 | 2 | 14-May-14 | 15-May-14 | 99 |
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - FRP Stairs LL2 | 6 | 6 | 02-Dec-13 | 09-Dec-13 | 12 |
| S3-4002 | Stair 3 - FRP Stairs LL1 | 6 | 6 | 10-Dec-13 | 17-Dec-13 | 12 |
| S3-4004 | Stair 3 - Permanent Railings / Final Finishes | 4 | 4 | 18-Dec-13 | 23-Dec-13 | 199 |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |
| S4-4000 | Stair 4 - FRP Stairs LL2 | 6 | 6 | 02-Dec-13 | 09-Dec-13 | 12 |
| S4-4002 | Stair 4 - FRP Stairs LL1 | 6 | 6 | 10-Dec-13 | 17-Dec-13 | 12 |
| S4-4004 | Stair 4 - FRP Stairs L1 | 6 | 6 | 03-Jan-14 | 14-Jan-14 | 56 |
| S4-4006 | Stair 4 - Permanent Railings / Final Finishes | 4 | 4 | 14-Jan-14 | 20-Jan-14 | 182 |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |

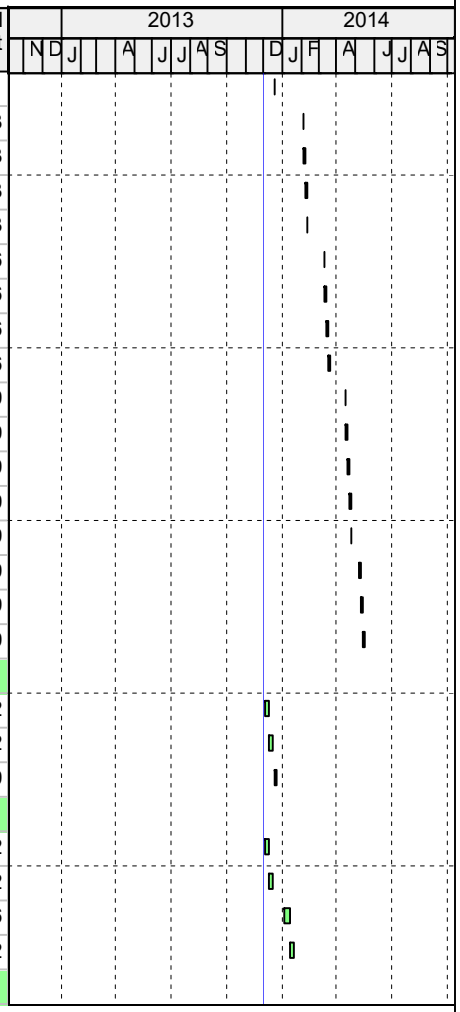



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S6-4000 | Stair 6 - FRP Stairs | 5 | 5 | 27-Dec-13 | 06-Jan-14 | 51 |
| S6-4002 | Stair 6 - Permanent Railings / Final Finishes | 2 | 2 | 06-Jan-14 | 08-Jan-14 | 189 |
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 4 | 27-Dec-13 | 03-Jan-14 | 192 |
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 10 | 06-Jan-14 | 21-Jan-14 | 51 |
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes | 5 | 5 | 21-Jan-14 | 28-Jan-14 | 176 |
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a - FRP Stairs L1 | 5 | 5 | 03-Jan-14 | 10-Jan-14 | 57 |
| S4a-4002 | Stair 4a - Permanent Railings / Final Finishes | 2 | 2 | 10-Jan-14 | 15-Jan-14 | 185 |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 07-Jun-13 A | | |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 0 | 17-Jun-13 A | 21-Jun-13 A | |
| EL-1004 | Elev - Submittal Approval | 21 | 1 | 21-Jun-13 A | 01-Dec-13 | 8 |
| EL-1006 | Elev - Release to Manufacturing | 14 | 14 | 02-Dec-13 | 15-Dec-13 | 8 |
| EL-1008 | Elev - Fabrication (Engineered Geared) | 120 | 120 | 16-Dec-13 | 14-Apr-14 | 8 |
| EL-1010 | Elev - Deliver to Jobsite | 1 | 1 | 15-Apr-14 | 15-Apr-14 | 6 |
| EL-1011 | Elev - Elevator Machines Flown & Set At Top Of Hoist | 9 | 9 | 16-Apr-14 | 28-Apr-14 | 6 |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 5 | 5 | 29-Apr-14 | 05-May-14 | 1 |
| EL-1202 | Elev 1&2 - Mob / Unload & Stage Equip / Materials | 5 | 5 | 29-Apr-14 | 05-May-14 | 1 |
| EL-3402 | Elev 3&4 - Mob / Unload & Stage Equip / Materials | 5 | 5 | 29-Apr-14 | 05-May-14 | 2 |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 5 | 5 | 29-Apr-14 | 05-May-14 | 64 |
| EL-5016 | Elev 5 - Hoistway Walls Complete (GC) | 0 | 0 | | 05-May-14 | 11 |
| EL-1216 | Elev 1&2 - Hoistway Walls Complete (GC) | 0 | 0 | | 05-May-14 | 1 |
| EL-3416 | Elev 3&4 - Hoistway Walls Complete (GC) | 0 | 0 | | 05-May-14 | 2 |
| EL-6016 | Elev 6 - Hoistway Walls Complete (GC) | 0 | 0 | | 05-May-14 | 64 |

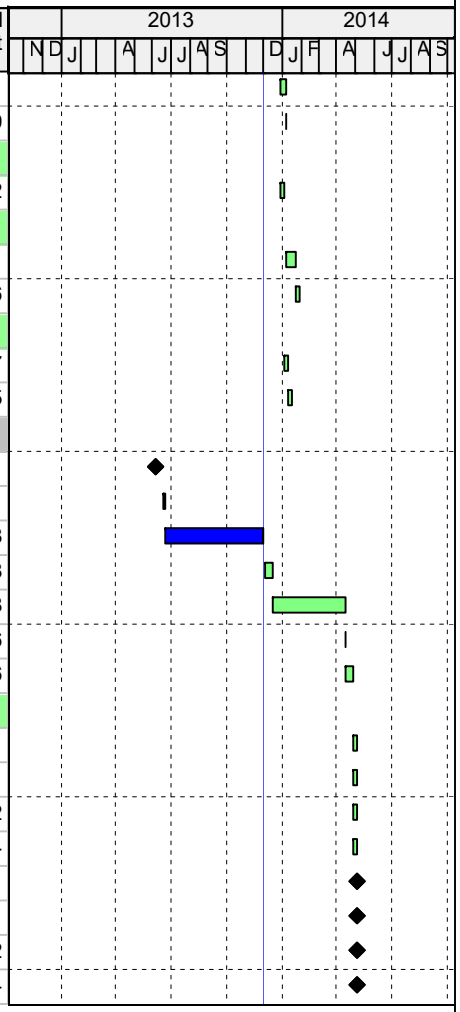



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 06-May-14 | | 1 |
| EL-5018 | Elev 5 - Install Machine Room Equipment | 5 | 5 | 06-May-14 | 12-May-14 | 11 |
| EL-1200 | Elev 1&2 - Hoistway Clear & Ready (GC) | 0 | 0 | 06-May-14 | | 1 |
| EL-1218 | Elev 1&2 - Install Machine Room Equipment | 5 | 5 | 06-May-14 | 12-May-14 | 1 |
| EL-3400 | Elev 3&4 - Hoistway Clear & Ready (GC) | 0 | 0 | 06-May-14 | | 2 |
| EL-3418 | Elev 3&4 - Install Machine Room Equipment | 5 | 5 | 06-May-14 | 12-May-14 | 2 |
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 06-May-14 | | 64 |
| EL-6018 | Elev 6 - Install Machine Room Equipment | 2 | 2 | 06-May-14 | 07-May-14 | 64 |
| EL-6004 | Elev 6 - Install Cylinders/Rails & Brackets | 4 | 4 | 08-May-14 | 13-May-14 | 64 |
| EL-5004 | Elev 5 - Install Rails & Brackets | 13 | 13 | 13-May-14 | 30-May-14 | 11 |
| EL-1204 | Elev 1&2 - Install Rails & Brackets | 17 | 17 | 13-May-14 | 05-Jun-14 | 1 |
| EL-3404 | Elev 3&4 - Install Rails & Brackets | 18 | 18 | 13-May-14 | 06-Jun-14 | 2 |
| EL-6006 | Elev 6 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 13-May-14 | 64 |
| EL-6007 | Elev 6 - Install Pit Equipment/Car Sling | 3 | 3 | 14-May-14 | 16-May-14 | 64 |
| EL-6010 | Elev 6 - Install Entrances/Doors/Fixtures/Fascia | 3 | 3 | 19-May-14 | 21-May-14 | 64 |
| EL-6012 | Elev 6 - Install Hoistway Equipment/Pipe & Wire | 2 | 2 | 22-May-14 | 23-May-14 | 64 |
| EL-6014 | Elev 6 - Install Cab/Wiring/Door Operator(s) | 5 | 5 | 27-May-14 | 02-Jun-14 | 64 |
| EL-5006 | Elev 5 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 30-May-14 | 11 |
| EL-5007 | Elev 5 - Install Pit Equipment/Car Sling/CWT Frame/V | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 11 |
| EL-6022 | Elev 6 - Adjust | 5 | 5 | 03-Jun-14 | 09-Jun-14 | 64 |
| EL-1206 | Elev 1&2 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 05-Jun-14 | 1 |
| EL-1207 | Elev 1&2 - Install Pit Equipment/Car Sling/CWT Fram | 3 | 3 | 06-Jun-14 | 10-Jun-14 | 1 |
| EL-3406 | Elev 3&4 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 06-Jun-14 | 2 |
| EL-5008 | Elev 5 - Install MHoist & Cable | 4 | 4 | 09-Jun-14 | 12-Jun-14 | 11 |
| EL-3407 | Elev 3&4 - Install Pit Equipment/Car Sling/CWT Fram | 5 | 5 | 09-Jun-14 | 13-Jun-14 | 2 |
| EL-6024 | Elev 6 - Clean / Paint / Punchlist | 1 | 1 | 10-Jun-14 | 10-Jun-14 | 64 |
| EL-1208 | Elev 1&2 - Install MHoist & Cable | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 1 |

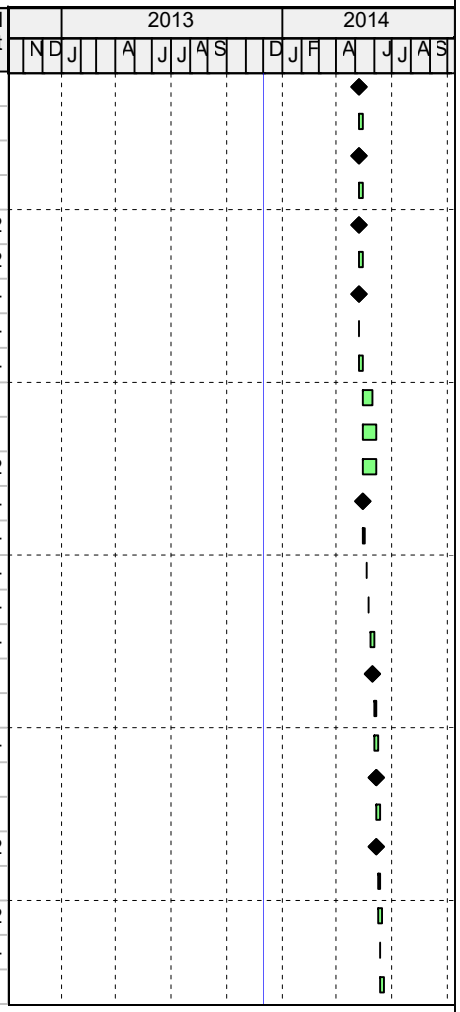



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6026 | Elev 6 - Inspections | 1 | 1 | 11-Jun-14 | 11-Jun-14 | 92 |
| EL-5010 | Elev 5 - Install Entrances/Doors/Fixtures/Fascia | 21 | 21 | 13-Jun-14 | 14-Jul-14 | 11 |
| EL-3408 | Elev 3&4 - Install Hoist & Cable | 5 | 5 | 16-Jun-14 | 20-Jun-14 | 2 |
| EL-1210 | Elev 1&2 - Install Entrances/Doors/Fixtures/Fascia | 19 | 19 | 18-Jun-14 | 15-Jul-14 | 1 |
| EL-3410 | Elev 3&4 - Install Entrances/Doors/Fixtures/Fascia | 30 | 30 | 23-Jun-14 | 04-Aug-14 | 2 |
| EL-5012 | Elev 5 - Install Hoistway Equipment/Pipe & Wire | 14 | 14 | 15-Jul-14 | 01-Aug-14 | 11 |
| EL-1212 | Elev 1&2 - Install Hoistway Equipment/Pipe & Wire | 17 | 17 | 16-Jul-14 | 07-Aug-14 | 1 |
| EL-5014 | Elev 5 - Install Cab/Wiring/Door Operator(s) | 7 | 7 | 04-Aug-14 | 12-Aug-14 | 11 |
| EL-3412 | Elev 3&4 - Install Hoistway Equipment/Pipe & Wire | 23 | 23 | 05-Aug-14 | 05-Sep-14 | 2 |
| EL-1214 | Elev 1&2 - Install Cab/Wiring/Door Operator(s) | 16 | 16 | 08-Aug-14 | 29-Aug-14 | 1 |
| EL-5022 | Elev 5 - Adjust | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 11 |
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 3 | 3 | 20-Aug-14 | 22-Aug-14 | 11 |
| EL-5026 | Elev 5 - Inspections | 2 | 2 | 23-Aug-14 | 24-Aug-14 | 18 |
| EL-1222 | Elev 1&2 - Adjust | 5 | 5 | 02-Sep-14 | 08-Sep-14 | 1 |
| EL-3414 | Elev 3&4 - Install Cab/Wiring/Door Operator(s) | 10 | 10 | 08-Sep-14 | 19-Sep-14 | 2 |
| EL-1224 | Elev 1&2 - Clean / Paint / Punchlist | 3 | 3 | 09-Sep-14 | 11-Sep-14 | 1 |
| EL-1226 | Elev 1&2 - Inspections | 2 | 2 | 12-Sep-14 | 13-Sep-14 | 3 |
| EL-3422 | Elev 3&4 - Adjust | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 2 |
| EL-3424 | Elev 3&4 - Clean / Paint / Punchlist | 3 | 3 | 29-Sep-14 | 01-Oct-14 | 2 |
| EL-3426 | Elev 3&4 - Inspections | 2 | 2 | 02-Oct-14 | 03-Oct-14 | 3 |
| **Exterior Shell** | | | | | | |
| **Elevations** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2** | | | | | | |
| L3-5308 | L3- Support Frame/Sheathing for Metal Wall Panels | 8 | 8 | 05-Feb-14 | 14-Feb-14 | 5 |
| L4-5308 | L4- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 12-Feb-14 | 18-Feb-14 | 5 |
| L5-5308 | L5- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 19-Feb-14 | 25-Feb-14 | 5 |

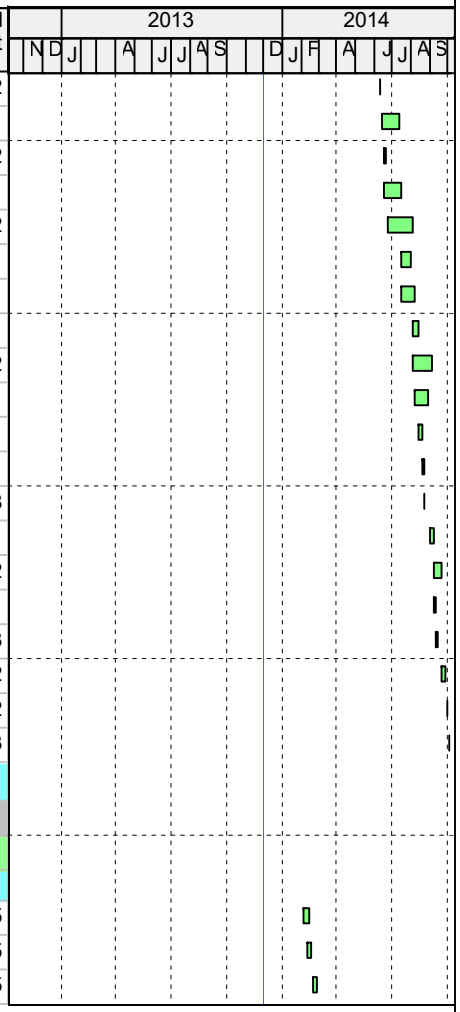



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L6-5308 | L6- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 26-Feb-14 | 04-Mar-14 | 5 |
| L7-5308 | L7- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 05-Mar-14 | 11-Mar-14 | 5 |
| LL2-5308 | LL2 Thru L4 - Support Frame/Sheathing for Metal Wa | 10 | 10 | 10-Mar-14 | 21-Mar-14 | 12 |
| L8-5308 | L8- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 12-Mar-14 | 18-Mar-14 | 5 |
| L9-5308 | L9- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 19-Mar-14 | 25-Mar-14 | 5 |
| LL1-5308 | LL1 - Support Frame/Sheathing for Metal Wall Panels | 10 | 10 | 24-Mar-14 | 04-Apr-14 | 13 |
| L10-5308 | L10- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 26-Mar-14 | 01-Apr-14 | 5 |
| LL2-5116 | LL2 Thru L4 - Metal Wall Panels (East/North) | 10 | 10 | 02-Apr-14 | 15-Apr-14 | 5 |
| L11-5308 | L11- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 02-Apr-14 | 08-Apr-14 | 5 |
| L1-5308 | L1 - Support Frame/Sheathing for Metal Wall Panels | 9 | 9 | 07-Apr-14 | 17-Apr-14 | 13 |
| L12-5308 | L12- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 16-Apr-14 | 22-Apr-14 | 0 |
| L14-5308 | L14 - Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 23-Apr-14 | 29-Apr-14 | 0 |
| L15-5308 | L15 - Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 30-Apr-14 | 06-May-14 | 0 |
| L16-5308 | L16- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 07-May-14 | 13-May-14 | 0 |
| L17-5308 | L17 - Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 14-May-14 | 20-May-14 | 0 |
| **Lower Level 1** | | | | | | |
| LL1-5116 | LL1 - Metal Wall Panels (East/North) | 10 | 10 | 16-Apr-14 | 29-Apr-14 | 5 |
| **Level 1** | | | | | | |
| L7-5116 | L7 - Metal Wall Panels | 5 | 5 | 19-Mar-14 | 25-Mar-14 | 136 |
| L1-5116 | L1 - Metal Wall Panels | 10 | 10 | 30-Apr-14 | 13-May-14 | 5 |
| L1-5102 | L1 - Storefront Frames | 10 | 10 | 14-May-14 | 28-May-14 | 86 |
| L3-5116 | L3 - Metal Wall Panels | 10 | 10 | 21-May-14 | 04-Jun-14 | 0 |
| L1-5104 | L1 - Storefront Glazing | 5 | 5 | 29-May-14 | 04-Jun-14 | 86 |
| EP-5110 | L1 - Revolving Doors | 5 | 5 | 29-May-14 | 04-Jun-14 | 86 |
| L3-5102 | L3- Storefront Frames | 10 | 10 | 05-Jun-14 | 18-Jun-14 | 71 |
| L4-5116 | L4 - Metal Wall Panels | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 0 |
| L5-5116 | L5 - Metal Wall Panels | 5 | 5 | 12-Jun-14 | 18-Jun-14 | 0 |

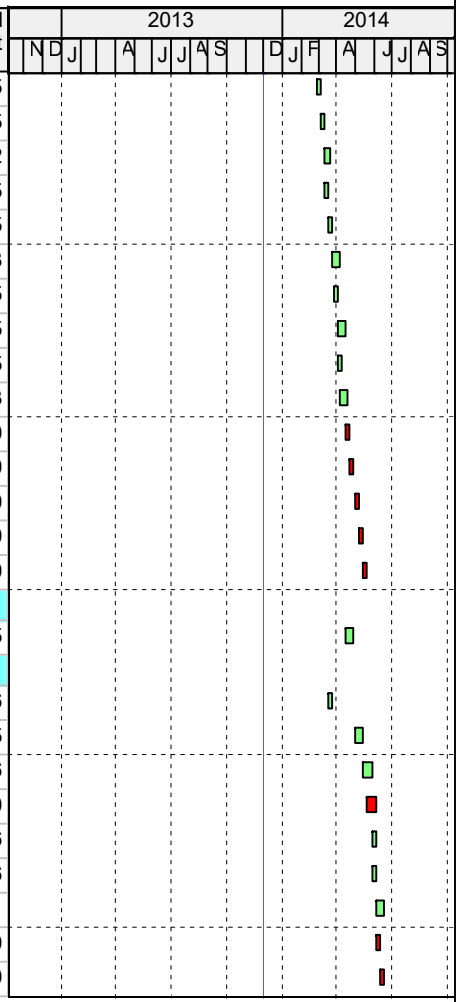



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L3-5104 | L3 - Storefront Glazing | 5 | 5 | 19-Jun-14 | 25-Jun-14 | 71 |
| L6-5116 | L6 - Metal Wall Panels | 5 | 5 | 19-Jun-14 | 25-Jun-14 | 0 |
| L8-5116 | L8 - Metal Wall Panels | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 0 |
| L9-5116 | L9 - Metal Wall Panels | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 0 |
| L10-5116 | L10 - Metal Wall Panels | 5 | 5 | 11-Jul-14 | 17-Jul-14 | 0 |
| L11-5116 | L11 - Metal Wall Panels | 5 | 5 | 18-Jul-14 | 24-Jul-14 | 0 |
| L12-5116 | L12 - Metal Wall Panels | 5 | 5 | 25-Jul-14 | 31-Jul-14 | 0 |
| L14-5116 | L14 - Metal Wall Panels | 5 | 5 | 01-Aug-14 | 07-Aug-14 | 0 |
| L15-5116 | L15 - Metal Wall Panels | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 0 |
| L16-5116 | L16 - Metal Wall Panels | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 0 |
| L17-5116 | L17 - Metal Wall Panels | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 0 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Levels 3-4** | | | | | | |
| L3-5130 | L3 - Install Punch Windows | 5 | 5 | 17-Feb-14 | 21-Feb-14 | 62 |
| L4-5130 | L4 - Install Punch Windows | 5 | 5 | 19-Feb-14 | 25-Feb-14 | 70 |
| L5-5130 | L5 - Install Punch Windows | 5 | 5 | 26-Feb-14 | 04-Mar-14 | 70 |
| L6-5130 | L6- Install Punch Windows | 5 | 5 | 05-Mar-14 | 11-Mar-14 | 70 |
| L7-5130 | L7 - Install Punch Windows | 5 | 5 | 12-Mar-14 | 18-Mar-14 | 136 |
| L8-5130 | L8 - Install Punch Windows | 5 | 5 | 19-Mar-14 | 25-Mar-14 | 65 |
| L9-5130 | L9 - Install Punch Windows | 5 | 5 | 26-Mar-14 | 01-Apr-14 | 65 |
| L10-5130 | L10 - Install Punch Windows | 5 | 5 | 02-Apr-14 | 08-Apr-14 | 65 |
| L11-5130 | L11 - Install Punch Windows | 5 | 5 | 09-Apr-14 | 15-Apr-14 | 65 |
| L12-5130 | L12 - Install Punch Windows | 5 | 5 | 23-Apr-14 | 29-Apr-14 | 60 |
| L14-5130 | L14 - Install Punch Windows | 5 | 5 | 30-Apr-14 | 06-May-14 | 60 |
| L15-5130 | L15 - Install Punch Windows | 5 | 5 | 07-May-14 | 13-May-14 | 60 |
| L16-5130 | L16 - Install Punch Windows | 5 | 5 | 14-May-14 | 20-May-14 | 60 |
| L17-5130 | L17 - Install Punch Windows | 5 | 5 | 21-May-14 | 28-May-14 | 60 |

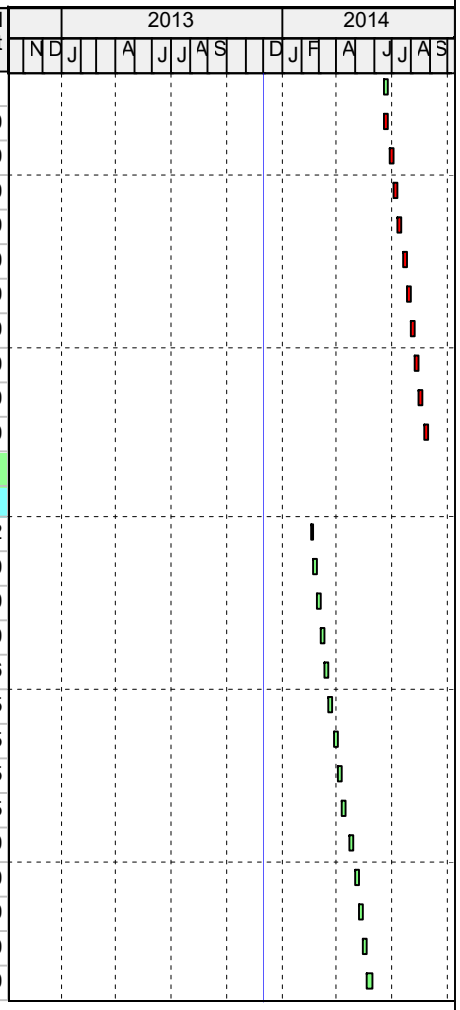



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| Roofs | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 5 | 06-Jan-14 | 10-Jan-14 | 67 |
| RF-4026 | L1 - City Park - Protection Board | 3 | 3 | 13-Jan-14 | 15-Jan-14 | 183 |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 2 | 16-Jan-14 | 17-Jan-14 | 183 |
| **Pool Membrane - (elev 18')** | | | | | | |
| RF-4034 | Pool Waterproofing / Membrane | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 0 |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 15 | 15 | 06-Mar-14 | 26-Mar-14 | 14 |
| RF-4010 | AR - Set Mechanical Equipment | 5 | 5 | 27-Mar-14 | 02-Apr-14 | 130 |
| RF-4012 | AR - Coping / Flashing | 4 | 4 | 27-Mar-14 | 01-Apr-14 | 53 |
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 5 | 5 | 27-Mar-14 | 02-Apr-14 | 9 |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |
| PC-4008 | RF - Entry / Porte Cochere Roofing System | 15 | 15 | 06-Mar-14 | 26-Mar-14 | 9 |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | Rf - Upper Ballroom Roofing System | 10 | 10 | 20-Feb-14 | 05-Mar-14 | 9 |
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 10 | 10 | 19-Jun-14 | 02-Jul-14 | 4 |
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |
| RF-4018 | TR - Terrace Roof - Roofing System | 5 | 5 | 01-Aug-14 | 07-Aug-14 | 36 |
| RF-4020 | TR - Terrace Roof - Coping / Flashing | 3 | 3 | 08-Aug-14 | 12-Aug-14 | 38 |
| RF-4022 | TR - Terrace Roof - Glass Railing | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 36 |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Substrates / Land Mech | 20 | 20 | 16-May-14 | 13-Jun-14 | 70 |
| RF-4002 | Tower Roof - Roofing / Roof Structures | 18 | 18 | 02-Jun-14 | 25-Jun-14 | 70 |
| **PH - Roof - (elev 173')** | | | | | | |

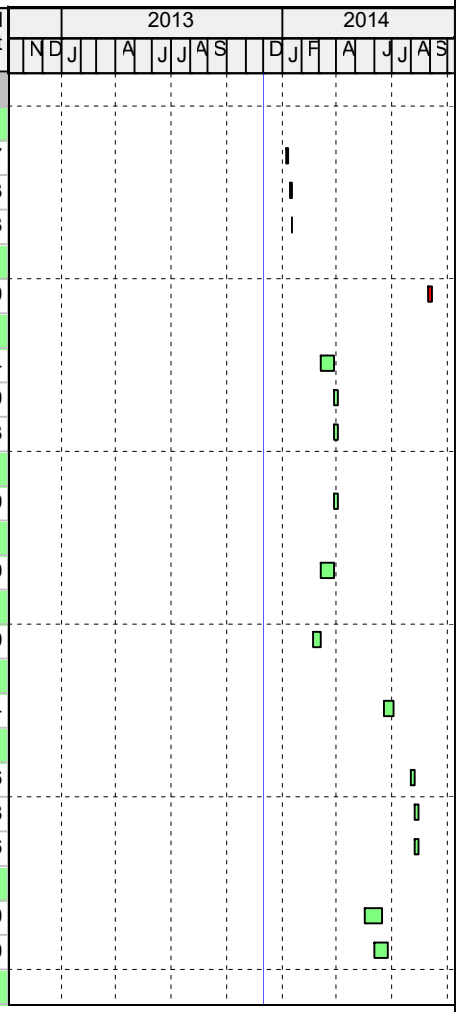



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| RF-4030 | PH - Roofing System | 5 | 5 | 29-Apr-14 | 05-May-14 | 1 |
| RF-4032 | PH - Coping / Flashing | 2 | 2 | 06-May-14 | 07-May-14 | 105 |
| **Rough-In's** | | | | | | |
| Lower Podium - (Levels LL2 / LL1 / 1 / 2) | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6002 | LL4 - Layout | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| LL4-6004 | LL4 - CMU Walls | 5 | 5 | 02-Dec-13 | 06-Dec-13 | 129 |
| LL4-6008 | LL4 - Int Wall Framing | 5 | 5 | 09-Dec-13 | 13-Dec-13 | 129 |
| LL4-6010 | LL4 - F/P Curbs | 5 | 5 | 09-Dec-13 | 13-Dec-13 | 139 |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 2 | 09-Dec-13 | 10-Dec-13 | 142 |
| LL4-6012 | LL4 - Fire Sprinkler Rl | 10 | 10 | 16-Dec-13 | 30-Dec-13 | 129 |
| LL4-6014 | LL4 - Plumbing Rl | 10 | 10 | 16-Dec-13 | 30-Dec-13 | 129 |
| LL4-6016 | LL4 - Electrical Rl | 10 | 10 | 16-Dec-13 | 30-Dec-13 | 129 |
| LL4-6018 | LL4 - HVAC Rl | 10 | 10 | 16-Dec-13 | 30-Dec-13 | 129 |
| LL4-6020 | LL4 - H Mtl Frames | 3 | 3 | 16-Dec-13 | 18-Dec-13 | 136 |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties Rl | 8 | 8 | 16-Dec-13 | 26-Dec-13 | 163 |
| LL4-6024 | LL4 - Inspections | 2 | 2 | 31-Dec-13 | 02-Jan-14 | 129 |
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6002 | LL3 - Layout | 1 | 0 | 19-Nov-13 A | 19-Nov-13 A | |
| LL3-6004 | LL3 - CMU Walls | 5 | 5 | 02-Dec-13 | 06-Dec-13 | 130 |
| LL3-6008 | LL3 - Int Wall Framing | 5 | 5 | 09-Dec-13 | 13-Dec-13 | 130 |
| LL3-6010 | LL3 - F/P Curbs | 5 | 5 | 09-Dec-13 | 13-Dec-13 | 140 |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 2 | 09-Dec-13 | 10-Dec-13 | 143 |
| LL3-6012 | LL3 - Fire Sprinkler Rl | 10 | 10 | 16-Dec-13 | 30-Dec-13 | 130 |
| LL3-6014 | LL3 - Plumbing Rl | 10 | 10 | 16-Dec-13 | 30-Dec-13 | 130 |
| LL3-6016 | LL3 - Electrical Rl | 10 | 10 | 16-Dec-13 | 30-Dec-13 | 130 |
| LL3-6018 | LL3 - HVAC Rl | 10 | 10 | 16-Dec-13 | 30-Dec-13 | 130 |

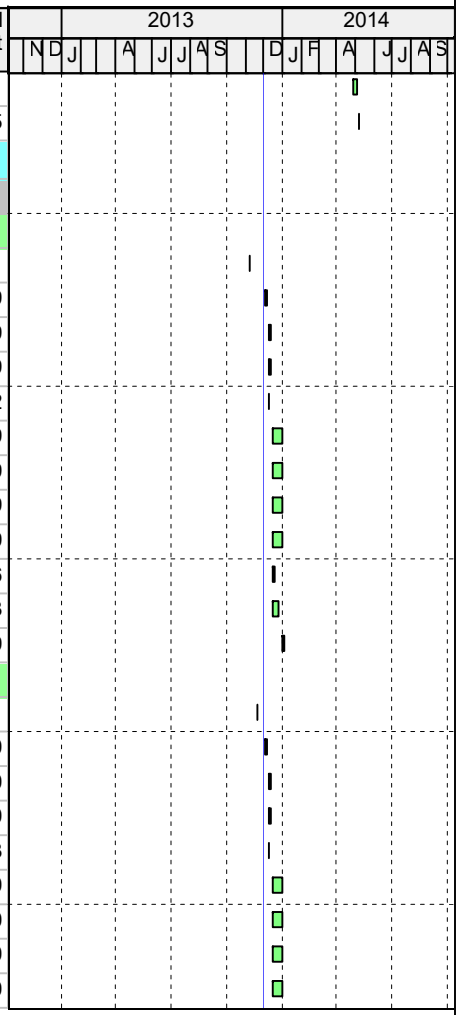



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-6020 | LL3 - H Mtl Frames | 3 | 3 | 16-Dec-13 | 18-Dec-13 | 137 |
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties RI | 8 | 8 | 16-Dec-13 | 26-Dec-13 | 168 |
| LL3-6024 | LL3 - Inspections | 2 | 2 | 31-Dec-13 | 02-Jan-14 | 130 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6002 | LL2 - Layout | 1 | 1 | 28-Feb-14 | 28-Feb-14 | 12 |
| LL2-6004 | LL2 - CMU Walls | 18 | 18 | 03-Mar-14 | 26-Mar-14 | 56 |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 3 | 03-Mar-14 | 05-Mar-14 | 12 |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 2 | 2 | 06-Mar-14 | 07-Mar-14 | 12 |
| LL2-6015 | LL2 - Main Elect Room Set Equip / RI - Power to Ma | 25 | 25 | 10-Mar-14 | 11-Apr-14 | 123 |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 5 | 27-Mar-14 | 02-Apr-14 | 56 |
| LL2-6010 | LL2 - F/P Curbs @ Parking | 5 | 5 | 27-Mar-14 | 02-Apr-14 | 118 |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 4 | 27-Mar-14 | 01-Apr-14 | 67 |
| LL2-6012 | LL2 - Fire Sprinkler RI | 10 | 10 | 03-Apr-14 | 16-Apr-14 | 56 |
| LL2-6014 | LL2 - Plumbing RI | 10 | 10 | 03-Apr-14 | 16-Apr-14 | 56 |
| LL2-6016 | LL2 - Electrical RI | 10 | 10 | 03-Apr-14 | 16-Apr-14 | 56 |
| LL2-6018 | LL2 - HVAC RI | 10 | 10 | 03-Apr-14 | 16-Apr-14 | 56 |
| LL2-6020 | LL2 - H Mtl Frames | 3 | 3 | 03-Apr-14 | 07-Apr-14 | 63 |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties RI | 8 | 8 | 03-Apr-14 | 14-Apr-14 | 87 |
| LL2-6024 | LL2 - Inspections | 2 | 2 | 17-Apr-14 | 18-Apr-14 | 56 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6002 | LL1 - Layout | 3 | 3 | 02-Jan-14 | 06-Jan-14 | 0 |
| LL1-6008 | LL1 - Int Wall Framing | 63 | 63 | 07-Jan-14 | 04-Apr-14 | 0 |
| LL1-6004 | LL1 - CMU Walls | 9 | 9 | 07-Jan-14 | 20-Jan-14 | 57 |
| LL1-6014 | LL1 - Plumbing RI | 63 | 63 | 09-Jan-14 | 08-Apr-14 | 3 |
| LL1-6018 | LL1 - HVAC RI | 63 | 63 | 09-Jan-14 | 08-Apr-14 | 3 |
| LL1-6012 | LL1 - Fire Sprinkler RI | 62 | 62 | 15-Jan-14 | 10-Apr-14 | 1 |

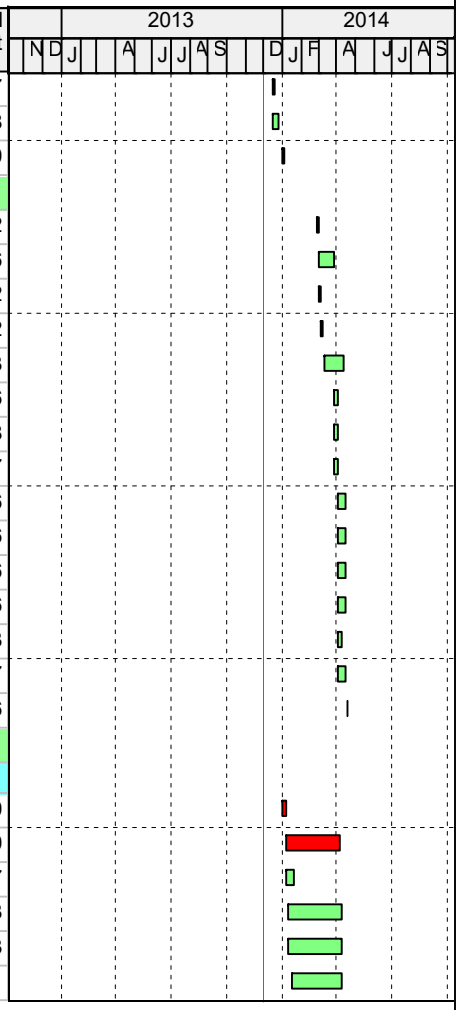



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-6016 | LL1 - Electrical RI | 62 | 62 | 15-Jan-14 | 10-Apr-14 | 1 |
| LL1-6010 | LL1 - CMU Seismic Clips | 2 | 2 | 21-Jan-14 | 22-Jan-14 | 57 |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 3 | 06-Mar-14 | 10-Mar-14 | 21 |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 3 | 3 | 11-Mar-14 | 13-Mar-14 | 21 |
| LL1-6020 | LL1 - H Mtl Frames | 5 | 5 | 07-Apr-14 | 11-Apr-14 | 0 |
| LL1-6022 | LL1 - Fire Alarm / Elec Specialties RI | 10 | 10 | 07-Apr-14 | 18-Apr-14 | 49 |
| LL1-6024 | LL1 - Inspections | 2 | 2 | 14-Apr-14 | 15-Apr-14 | 0 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-6002 | L1 - Layout | 1 | 1 | 03-Jan-14 | 06-Jan-14 | 53 |
| L01-6004 | L1 - CMU Walls | 8 | 8 | 06-Jan-14 | 17-Jan-14 | 53 |
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 5 | 06-Jan-14 | 14-Jan-14 | 71 |
| L01-6010 | L1 - CMU Seismic Clips | 1 | 1 | 17-Jan-14 | 20-Jan-14 | 97 |
| L01-6008 | L1 - Int Wall Framing | 25 | 25 | 14-Mar-14 | 17-Apr-14 | 14 |
| L01-6012 | L1 - Fire Sprinkler RI | 25 | 25 | 21-Mar-14 | 24-Apr-14 | 29 |
| L01-6014 | L1 - Plumbing RI | 20 | 20 | 21-Mar-14 | 17-Apr-14 | 34 |
| L01-6016 | L1 - Electrical RI | 25 | 25 | 21-Mar-14 | 24-Apr-14 | 29 |
| L01-6018 | L1 - HVAC RI | 40 | 40 | 21-Mar-14 | 15-May-14 | 14 |
| L01-6020 | L1 - H Mtl Frames | 5 | 5 | 18-Apr-14 | 24-Apr-14 | 29 |
| L01-6022 | L1 - Fire Alarm / Elec Specialties RI | 10 | 10 | 18-Apr-14 | 01-May-14 | 60 |
| L01-6024 | L1 - Inspections | 2 | 2 | 16-May-14 | 19-May-14 | 14 |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6002 | L2 - Layout | 1 | 1 | 22-Jan-14 | 22-Jan-14 | 45 |
| L02-6004 | L2 - CMU Walls | 5 | 5 | 23-Jan-14 | 29-Jan-14 | 45 |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 1 | 30-Jan-14 | 30-Jan-14 | 79 |
| L02-6008 | L2 - Int Wall Framing | 25 | 25 | 04-Mar-14 | 07-Apr-14 | 22 |
| L02-6014 | L2 - Plumbing RI | 22 | 22 | 11-Mar-14 | 09-Apr-14 | 30 |
| L02-6016 | L2 - Electrical RI | 22 | 22 | 11-Mar-14 | 09-Apr-14 | 30 |

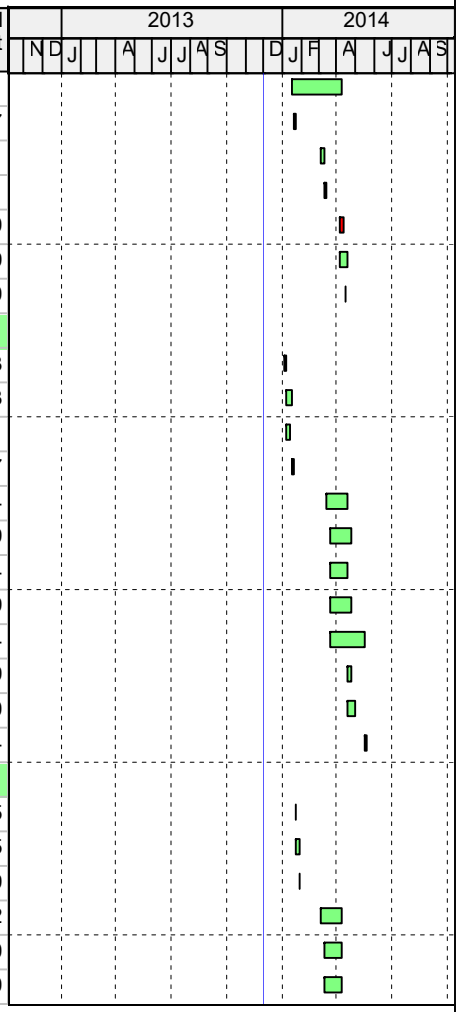



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 5 | 11-Mar-14 | 17-Mar-14 | 22 |
| L02-6012 | L2 - Fire Sprinkler RI | 20 | 20 | 13-Mar-14 | 09-Apr-14 | 30 |
| L02-6018 | L2 - HVAC RI | 30 | 30 | 13-Mar-14 | 23-Apr-14 | 20 |
| L02-6006 | L2 - Ext Wall Framing - (Cold Formed) | 10 | 10 | 18-Mar-14 | 31-Mar-14 | 22 |
| L02-6020 | L2 - H Mtl Frames | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 44 |
| L02-6022 | L2 - Fire Alarm / Elec Specialties RI | 10 | 10 | 08-Apr-14 | 21-Apr-14 | 72 |
| L02-6024 | L2 - Inspections | 2 | 2 | 24-Apr-14 | 25-Apr-14 | 20 |
| Upper Tower - (Levels 3 thru PH) | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L03-8219 | HVAC Risers | 5 | 5 | 26-Dec-13 | 03-Jan-14 | 192 |
| L03-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 26-Dec-13 | 03-Jan-14 | 120 |
| L03-6008 | Frame Shaft Walls | 3 | 3 | 03-Jan-14 | 08-Jan-14 | 120 |
| L04-8219 | HVAC Risers | 5 | 5 | 07-Jan-14 | 14-Jan-14 | 186 |
| L04-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 07-Jan-14 | 14-Jan-14 | 114 |
| L03-6009 | Inspect Shafts | 1 | 1 | 08-Jan-14 | 09-Jan-14 | 120 |
| L03-6011 | PreRock Shafts | 2 | 2 | 09-Jan-14 | 14-Jan-14 | 122 |
| L03-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 10-Jan-14 | 14-Jan-14 | 122 |
| L03-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 14-Jan-14 | 15-Jan-14 | 185 |
| L04-6008 | Frame Shaft Walls | 3 | 3 | 15-Jan-14 | 17-Jan-14 | 114 |
| L05-8219 | HVAC Risers | 5 | 5 | 16-Jan-14 | 22-Jan-14 | 180 |
| L05-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 16-Jan-14 | 22-Jan-14 | 108 |
| L04-6009 | Inspect Shafts | 1 | 1 | 20-Jan-14 | 20-Jan-14 | 114 |
| L04-6011 | PreRock Shafts | 2 | 2 | 21-Jan-14 | 22-Jan-14 | 116 |
| L04-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 22-Jan-14 | 22-Jan-14 | 116 |
| L04-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 23-Jan-14 | 23-Jan-14 | 179 |
| L05-6008 | Frame Shaft Walls | 3 | 3 | 23-Jan-14 | 27-Jan-14 | 108 |
| L06-8219 | HVAC Risers | 5 | 5 | 23-Jan-14 | 29-Jan-14 | 175 |

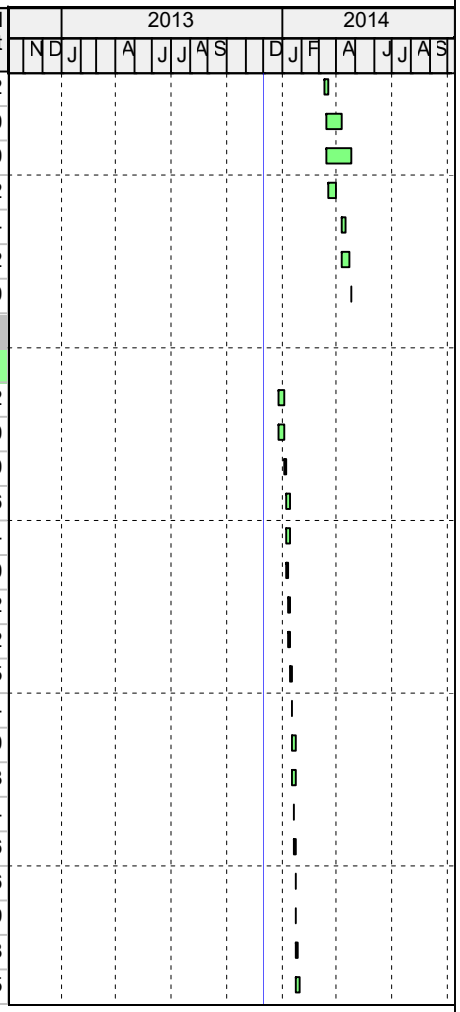



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 23-Jan-14 | 29-Jan-14 | 103 |
| L05-6009 | Inspect Shafts | 1 | 1 | 28-Jan-14 | 28-Jan-14 | 108 |
| L05-6011 | PreRock Shafts | 2 | 2 | 29-Jan-14 | 30-Jan-14 | 110 |
| L05-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 30-Jan-14 | 30-Jan-14 | 110 |
| L06-6008 | Frame Shaft Walls | 3 | 3 | 30-Jan-14 | 03-Feb-14 | 103 |
| L07-8219 | HVAC Risers | 5 | 5 | 30-Jan-14 | 05-Feb-14 | 170 |
| L07-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 30-Jan-14 | 05-Feb-14 | 98 |
| L05-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 31-Jan-14 | 31-Jan-14 | 173 |
| L06-6009 | Inspect Shafts | 1 | 1 | 04-Feb-14 | 04-Feb-14 | 103 |
| L03-6002 | Layout | 5 | 5 | 05-Feb-14 | 11-Feb-14 | 100 |
| L06-6011 | PreRock Shafts | 2 | 2 | 05-Feb-14 | 06-Feb-14 | 105 |
| L06-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 06-Feb-14 | 06-Feb-14 | 105 |
| L07-6008 | Frame Shaft Walls | 3 | 3 | 06-Feb-14 | 10-Feb-14 | 98 |
| L08-8219 | HVAC Risers | 5 | 5 | 06-Feb-14 | 12-Feb-14 | 165 |
| L08-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 06-Feb-14 | 12-Feb-14 | 93 |
| L06-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 07-Feb-14 | 07-Feb-14 | 168 |
| L07-6009 | Inspect Shafts | 1 | 1 | 11-Feb-14 | 11-Feb-14 | 98 |
| L03-6004 | CMU Wall/Clips | 3 | 3 | 12-Feb-14 | 14-Feb-14 | 163 |
| L04-6002 | Layout | 5 | 5 | 12-Feb-14 | 18-Feb-14 | 95 |
| L07-6011 | PreRock Shafts | 2 | 2 | 12-Feb-14 | 13-Feb-14 | 100 |
| L07-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 13-Feb-14 | 13-Feb-14 | 100 |
| L08-6008 | Frame Shaft Walls | 3 | 3 | 13-Feb-14 | 17-Feb-14 | 93 |
| L09-8219 | HVAC Risers | 5 | 5 | 13-Feb-14 | 19-Feb-14 | 160 |
| L09-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 13-Feb-14 | 19-Feb-14 | 88 |
| L07-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 14-Feb-14 | 14-Feb-14 | 163 |
| L03-6010 | Frame Walls | 5 | 5 | 18-Feb-14 | 24-Feb-14 | 93 |
| L03-6023 | Inspection of Exterior Framing | 0 | 0 | 18-Feb-14 | | 92 |

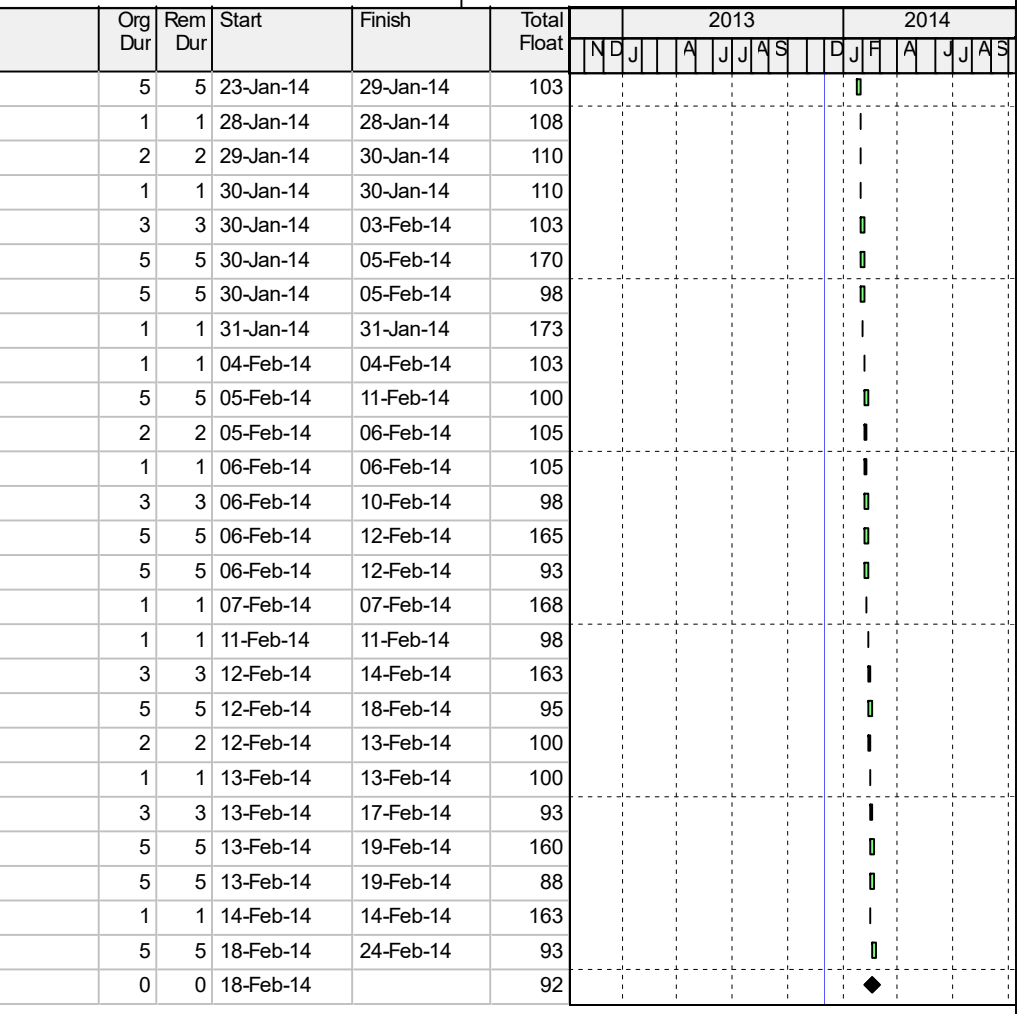



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-6009 | Inspect Shafts | 1 | 1 | 18-Feb-14 | 18-Feb-14 | 93 |
| L03-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 19-Feb-14 | 19-Feb-14 | 92 |
| L04-6004 | CMU Wall/Clips | 3 | 3 | 19-Feb-14 | 21-Feb-14 | 158 |
| L04-6010 | Frame Walls | 5 | 5 | 19-Feb-14 | 25-Feb-14 | 92 |
| L04-6023 | Inspection of Exterior Framing | 0 | 0 | 19-Feb-14 | | 91 |
| L05-6002 | Layout | 5 | 5 | 19-Feb-14 | 25-Feb-14 | 90 |
| L08-6011 | PreRock Shafts | 2 | 2 | 19-Feb-14 | 20-Feb-14 | 95 |
| L03-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 20-Feb-14 | 20-Feb-14 | 92 |
| L04-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 20-Feb-14 | 20-Feb-14 | 91 |
| L08-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 20-Feb-14 | 20-Feb-14 | 95 |
| L09-6008 | Frame Shaft Walls | 3 | 3 | 20-Feb-14 | 24-Feb-14 | 88 |
| L10-8219 | HVAC Risers | 5 | 5 | 20-Feb-14 | 26-Feb-14 | 155 |
| L10-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 20-Feb-14 | 26-Feb-14 | 83 |
| L03-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 21-Feb-14 | 21-Feb-14 | 92 |
| L04-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 21-Feb-14 | 21-Feb-14 | 91 |
| L08-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 21-Feb-14 | 21-Feb-14 | 158 |
| L03-6012 | Fire Sprinkler Mains | 5 | 5 | 24-Feb-14 | 28-Feb-14 | 93 |
| L03-6014 | Set Tubs & Plumbing Rl | 5 | 5 | 24-Feb-14 | 28-Feb-14 | 93 |
| L03-6016 | Electrical Rl | 5 | 5 | 24-Feb-14 | 28-Feb-14 | 93 |
| L03-6018 | HVAC Rl | 5 | 5 | 24-Feb-14 | 28-Feb-14 | 93 |
| L03-6022 | Fire Alarm / Elec Specialties Rl | 5 | 5 | 24-Feb-14 | 28-Feb-14 | 93 |
| L03-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 24-Feb-14 | 24-Feb-14 | 92 |
| L04-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 24-Feb-14 | 24-Feb-14 | 91 |
| L03-6020 | Install Hollow Metal Frames | 3 | 3 | 25-Feb-14 | 27-Feb-14 | 97 |
| L03-6019 | Complete Top Out GWB | 2 | 2 | 25-Feb-14 | 26-Feb-14 | 93 |
| L03-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 25-Feb-14 | 25-Feb-14 | 92 |
| L04-6012 | Fire Sprinkler Mains | 5 | 5 | 25-Feb-14 | 03-Mar-14 | 92 |

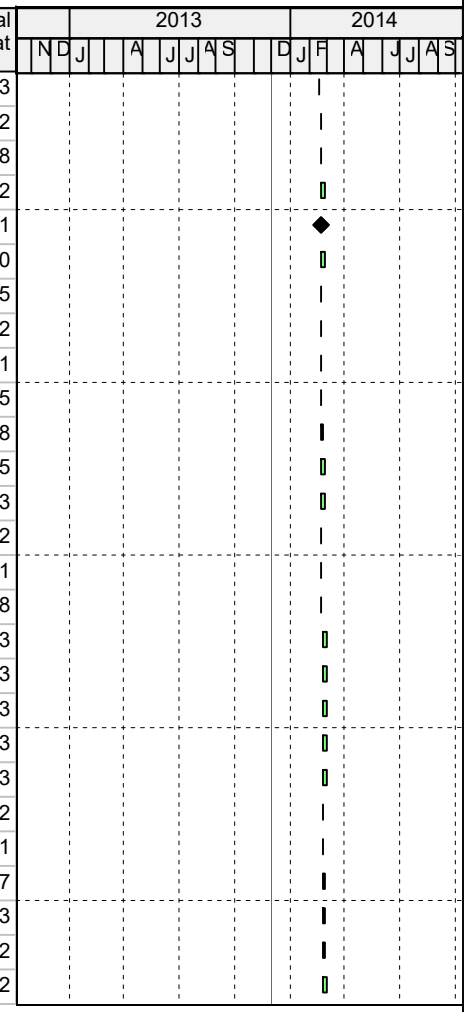



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6014 | Set Tubs & Plumbing Rl | 5 | 5 | 25-Feb-14 | 03-Mar-14 | 92 |
| L04-6016 | Electrical Rl | 5 | 5 | 25-Feb-14 | 03-Mar-14 | 92 |
| L04-6018 | HVAC Rl | 5 | 5 | 25-Feb-14 | 03-Mar-14 | 92 |
| L04-6022 | Fire Alarm / Elec Specialties Rl | 5 | 5 | 25-Feb-14 | 03-Mar-14 | 92 |
| L04-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 25-Feb-14 | 25-Feb-14 | 91 |
| L09-6009 | Inspect Shafts | 1 | 1 | 25-Feb-14 | 25-Feb-14 | 88 |
| L03-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 26-Feb-14 | 28-Feb-14 | 93 |
| L03-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 26-Feb-14 | 26-Feb-14 | 92 |
| L04-6020 | Install Hollow Metal Frames | 3 | 3 | 26-Feb-14 | 28-Feb-14 | 96 |
| L04-6019 | Complete Top Out GWB | 2 | 2 | 26-Feb-14 | 27-Feb-14 | 92 |
| L04-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 26-Feb-14 | 26-Feb-14 | 91 |
| L05-6004 | CMU Wall/Clips | 3 | 3 | 26-Feb-14 | 28-Feb-14 | 153 |
| L05-6010 | Frame Walls | 5 | 5 | 26-Feb-14 | 04-Mar-14 | 87 |
| L05-6023 | Inspection of Exterior Framing | 0 | 0 | 26-Feb-14 | | 86 |
| L06-6002 | Layout | 5 | 5 | 26-Feb-14 | 04-Mar-14 | 85 |
| L09-6011 | PreRock Shafts | 2 | 2 | 26-Feb-14 | 27-Feb-14 | 90 |
| L03-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 27-Feb-14 | 03-Mar-14 | 93 |
| L03-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 27-Feb-14 | 04-Mar-14 | 92 |
| L04-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 27-Feb-14 | 03-Mar-14 | 92 |
| L04-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 27-Feb-14 | 27-Feb-14 | 91 |
| L05-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 27-Feb-14 | 27-Feb-14 | 86 |
| L09-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 27-Feb-14 | 27-Feb-14 | 90 |
| L10-6008 | Frame Shaft Walls | 3 | 3 | 27-Feb-14 | 03-Mar-14 | 83 |
| L11-8219 | HVAC Risers | 5 | 5 | 27-Feb-14 | 05-Mar-14 | 150 |
| L11-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 27-Feb-14 | 05-Mar-14 | 38 |
| L03-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 28-Feb-14 | 03-Mar-14 | 92 |
| L04-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 28-Feb-14 | 04-Mar-14 | 92 |

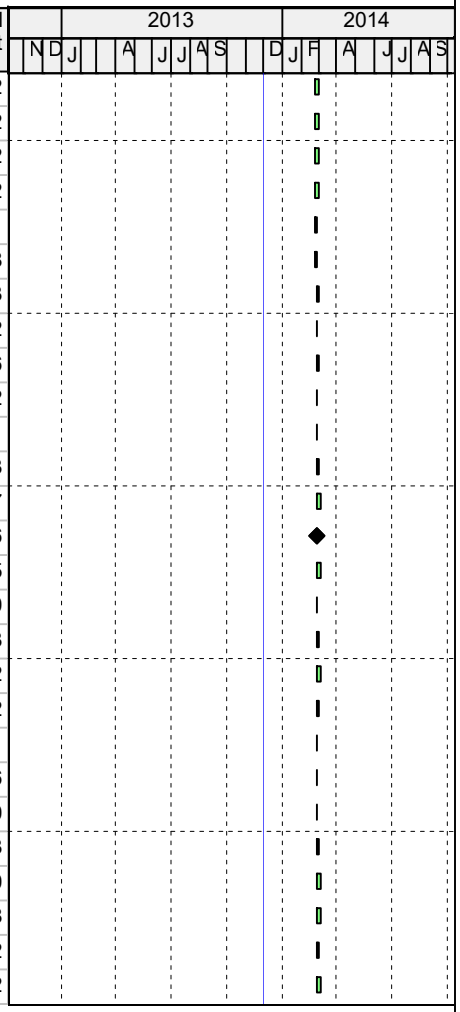



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 28-Feb-14 | 05-Mar-14 | 91 |
| L05-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 28-Feb-14 | 28-Feb-14 | 86 |
| L09-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 28-Feb-14 | 28-Feb-14 | 153 |
| L04-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 03-Mar-14 | 04-Mar-14 | 91 |
| L05-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 03-Mar-14 | 03-Mar-14 | 86 |
| L03-6024 | Inspections for GWB Cover | 1 | 1 | 04-Mar-14 | 04-Mar-14 | 92 |
| L05-6012 | Fire Sprinkler Mains | 5 | 5 | 04-Mar-14 | 10-Mar-14 | 87 |
| L05-6014 | Set Tubs & Plumbing RI | 5 | 5 | 04-Mar-14 | 10-Mar-14 | 87 |
| L05-6016 | Electrical RI | 5 | 5 | 04-Mar-14 | 10-Mar-14 | 87 |
| L05-6018 | HVAC RI | 5 | 5 | 04-Mar-14 | 10-Mar-14 | 87 |
| L05-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 04-Mar-14 | 10-Mar-14 | 87 |
| L05-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 04-Mar-14 | 04-Mar-14 | 86 |
| L10-6009 | Inspect Shafts | 1 | 1 | 04-Mar-14 | 04-Mar-14 | 83 |
| L04-6024 | Inspections for GWB Cover | 1 | 1 | 05-Mar-14 | 05-Mar-14 | 91 |
| L05-6020 | Install Hollow Metal Frames | 3 | 3 | 05-Mar-14 | 07-Mar-14 | 91 |
| L05-6019 | Complete Top Out GWB | 2 | 2 | 05-Mar-14 | 06-Mar-14 | 87 |
| L05-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 05-Mar-14 | 05-Mar-14 | 86 |
| L06-6004 | CMU Wall/Clips | 3 | 3 | 05-Mar-14 | 07-Mar-14 | 148 |
| L06-6010 | Frame Walls | 5 | 5 | 05-Mar-14 | 11-Mar-14 | 82 |
| L06-6023 | Inspection of Exterior Framing | 0 | 0 | 05-Mar-14 | | 81 |
| L07-6002 | Layout | 5 | 5 | 05-Mar-14 | 11-Mar-14 | 80 |
| L10-6011 | PreRock Shafts | 2 | 2 | 05-Mar-14 | 06-Mar-14 | 85 |
| L05-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 06-Mar-14 | 10-Mar-14 | 87 |
| L05-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 06-Mar-14 | 06-Mar-14 | 86 |
| L06-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 06-Mar-14 | 06-Mar-14 | 81 |
| L10-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 06-Mar-14 | 06-Mar-14 | 85 |
| L11-6008 | Frame Shaft Walls | 3 | 3 | 06-Mar-14 | 10-Mar-14 | 38 |

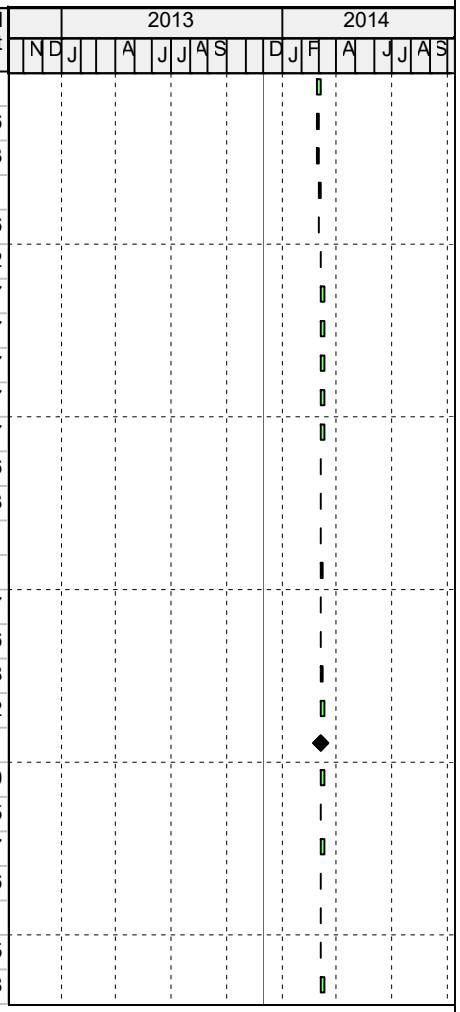



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8219 | HVAC Risers | 5 | 5 | 06-Mar-14 | 12-Mar-14 | 145 |
| L12-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 06-Mar-14 | 12-Mar-14 | 73 |
| L05-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 07-Mar-14 | 11-Mar-14 | 87 |
| L05-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 07-Mar-14 | 12-Mar-14 | 86 |
| L06-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 07-Mar-14 | 07-Mar-14 | 81 |
| L10-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 07-Mar-14 | 07-Mar-14 | 148 |
| L05-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 10-Mar-14 | 11-Mar-14 | 86 |
| L06-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 10-Mar-14 | 10-Mar-14 | 81 |
| L06-6012 | Fire Sprinkler Mains | 5 | 5 | 11-Mar-14 | 17-Mar-14 | 82 |
| L06-6014 | Set Tubs & Plumbing RI | 5 | 5 | 11-Mar-14 | 17-Mar-14 | 82 |
| L06-6016 | Electrical RI | 5 | 5 | 11-Mar-14 | 17-Mar-14 | 82 |
| L06-6018 | HVAC RI | 5 | 5 | 11-Mar-14 | 17-Mar-14 | 82 |
| L06-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 11-Mar-14 | 17-Mar-14 | 82 |
| L06-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 11-Mar-14 | 11-Mar-14 | 81 |
| L11-6009 | Inspect Shafts | 1 | 1 | 11-Mar-14 | 11-Mar-14 | 38 |
| L05-6024 | Inspections for GWB Cover | 1 | 1 | 12-Mar-14 | 12-Mar-14 | 86 |
| L06-6020 | Install Hollow Metal Frames | 3 | 3 | 12-Mar-14 | 14-Mar-14 | 86 |
| L06-6019 | Complete Top Out GWB | 2 | 2 | 12-Mar-14 | 13-Mar-14 | 82 |
| L06-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 12-Mar-14 | 12-Mar-14 | 81 |
| L07-6004 | CMU Wall/Clips | 3 | 3 | 12-Mar-14 | 14-Mar-14 | 143 |
| L07-6010 | Frame Walls | 5 | 5 | 12-Mar-14 | 18-Mar-14 | 77 |
| L07-6023 | Inspection of Exterior Framing | 0 | 0 | 12-Mar-14 | | 76 |
| L08-6002 | Layout | 5 | 5 | 12-Mar-14 | 18-Mar-14 | 75 |
| L11-6011 | PreRock Shafts | 2 | 2 | 12-Mar-14 | 13-Mar-14 | 40 |
| L06-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 13-Mar-14 | 17-Mar-14 | 82 |
| L06-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 13-Mar-14 | 13-Mar-14 | 81 |
| L07-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 13-Mar-14 | 13-Mar-14 | 76 |

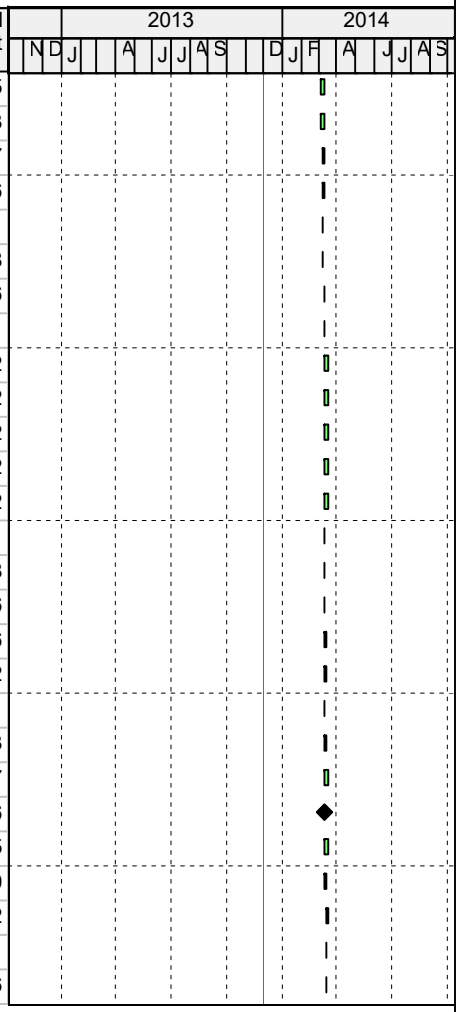



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 13-Mar-14 | 13-Mar-14 | 40 |
| L12-6008 | Frame Shaft Walls | 3 | 3 | 13-Mar-14 | 17-Mar-14 | 73 |
| L14-8219 | HVAC Risers | 5 | 5 | 13-Mar-14 | 19-Mar-14 | 140 |
| L14-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 13-Mar-14 | 19-Mar-14 | 68 |
| L06-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 14-Mar-14 | 18-Mar-14 | 82 |
| L06-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 14-Mar-14 | 19-Mar-14 | 81 |
| L07-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 14-Mar-14 | 14-Mar-14 | 76 |
| L11-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 14-Mar-14 | 14-Mar-14 | 143 |
| L03-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 17-Mar-14 | 25-Mar-14 | 92 |
| L06-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 17-Mar-14 | 18-Mar-14 | 81 |
| L07-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 17-Mar-14 | 17-Mar-14 | 76 |
| L04-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 18-Mar-14 | 26-Mar-14 | 91 |
| L07-6012 | Fire Sprinkler Mains | 5 | 5 | 18-Mar-14 | 24-Mar-14 | 77 |
| L07-6014 | Set Tubs & Plumbing RI | 5 | 5 | 18-Mar-14 | 24-Mar-14 | 77 |
| L07-6016 | Electrical RI | 5 | 5 | 18-Mar-14 | 24-Mar-14 | 77 |
| L07-6018 | HVAC RI | 5 | 5 | 18-Mar-14 | 24-Mar-14 | 77 |
| L07-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 18-Mar-14 | 24-Mar-14 | 77 |
| L07-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 18-Mar-14 | 18-Mar-14 | 76 |
| L12-6009 | Inspect Shafts | 1 | 1 | 18-Mar-14 | 18-Mar-14 | 73 |
| L06-6024 | Inspections for GWB Cover | 1 | 1 | 19-Mar-14 | 19-Mar-14 | 81 |
| L07-6020 | Install Hollow Metal Frames | 3 | 3 | 19-Mar-14 | 21-Mar-14 | 81 |
| L07-6019 | Complete Top Out GWB | 2 | 2 | 19-Mar-14 | 20-Mar-14 | 77 |
| L07-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 19-Mar-14 | 19-Mar-14 | 76 |
| L08-6004 | CMU Wall/Clips | 3 | 3 | 19-Mar-14 | 21-Mar-14 | 138 |
| L08-6010 | Frame Walls | 5 | 5 | 19-Mar-14 | 25-Mar-14 | 72 |
| L08-6023 | Inspection of Exterior Framing | 0 | 0 | 19-Mar-14 | | 71 |
| L09-6002 | Layout | 5 | 5 | 19-Mar-14 | 25-Mar-14 | 70 |

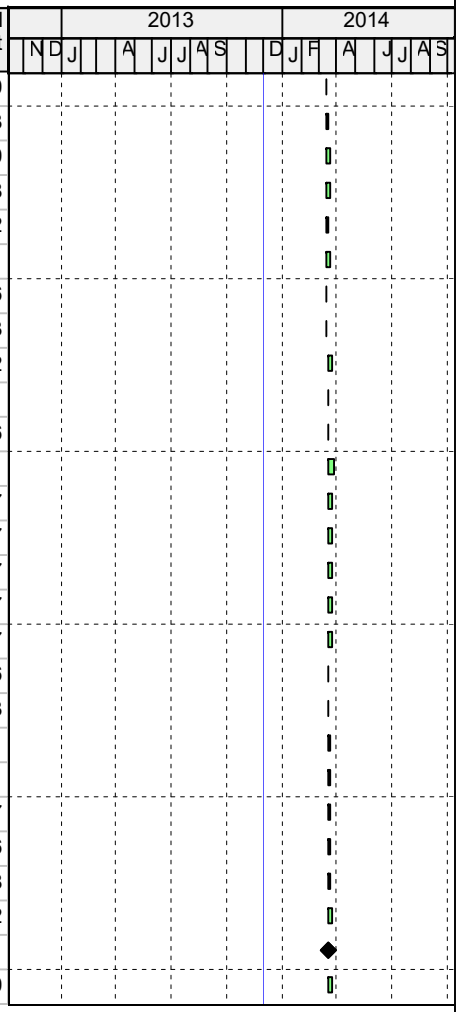



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-6011 | PreRock Shafts | 2 | 2 | 19-Mar-14 | 20-Mar-14 | 75 |
| L07-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 20-Mar-14 | 24-Mar-14 | 77 |
| L07-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 20-Mar-14 | 20-Mar-14 | 76 |
| L08-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 20-Mar-14 | 20-Mar-14 | 71 |
| L12-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 20-Mar-14 | 20-Mar-14 | 75 |
| L14-6008 | Frame Shaft Walls | 3 | 3 | 20-Mar-14 | 24-Mar-14 | 68 |
| L15-8219 | HVAC Risers | 5 | 5 | 20-Mar-14 | 26-Mar-14 | 135 |
| L15-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 20-Mar-14 | 26-Mar-14 | 63 |
| L07-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 21-Mar-14 | 25-Mar-14 | 77 |
| L07-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 21-Mar-14 | 26-Mar-14 | 76 |
| L08-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 21-Mar-14 | 21-Mar-14 | 71 |
| L12-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 21-Mar-14 | 21-Mar-14 | 138 |
| L07-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 24-Mar-14 | 25-Mar-14 | 76 |
| L08-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 24-Mar-14 | 24-Mar-14 | 71 |
| L05-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 25-Mar-14 | 02-Apr-14 | 86 |
| L08-6012 | Fire Sprinkler Mains | 5 | 5 | 25-Mar-14 | 31-Mar-14 | 72 |
| L08-6014 | Set Tubs & Plumbing RI | 5 | 5 | 25-Mar-14 | 31-Mar-14 | 72 |
| L08-6016 | Electrical RI | 5 | 5 | 25-Mar-14 | 31-Mar-14 | 72 |
| L08-6018 | HVAC RI | 5 | 5 | 25-Mar-14 | 31-Mar-14 | 72 |
| L08-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 25-Mar-14 | 31-Mar-14 | 72 |
| L08-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 25-Mar-14 | 25-Mar-14 | 71 |
| L14-6009 | Inspect Shafts | 1 | 1 | 25-Mar-14 | 25-Mar-14 | 68 |
| L07-6024 | Inspections for GWB Cover | 1 | 1 | 26-Mar-14 | 26-Mar-14 | 76 |
| L08-6020 | Install Hollow Metal Frames | 3 | 3 | 26-Mar-14 | 28-Mar-14 | 76 |
| L08-6019 | Complete Top Out GWB | 2 | 2 | 26-Mar-14 | 27-Mar-14 | 72 |
| L08-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 26-Mar-14 | 26-Mar-14 | 71 |
| L09-6004 | CMU Wall/Clips | 3 | 3 | 26-Mar-14 | 28-Mar-14 | 133 |

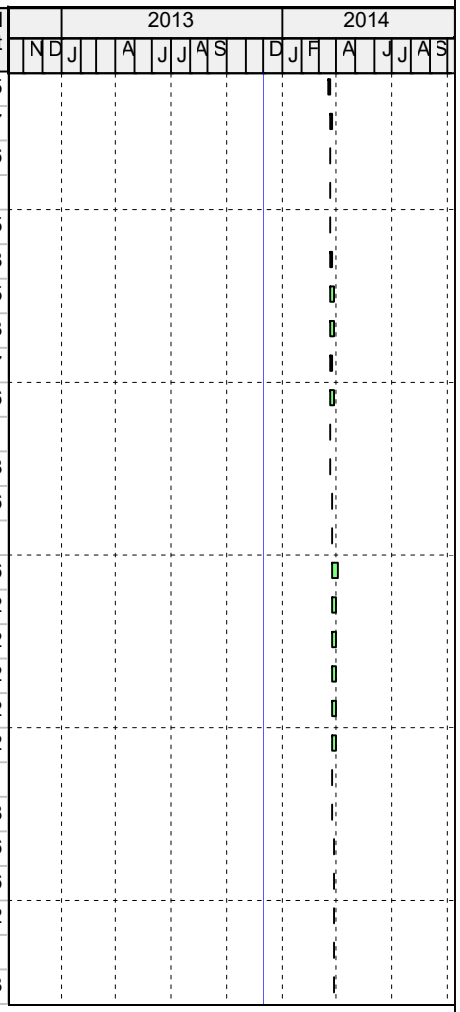



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6010 | Frame Walls | 5 | 5 | 26-Mar-14 | 01-Apr-14 | 67 |
| L09-6023 | Inspection of Exterior Framing | 0 | 0 | 26-Mar-14 | | 66 |
| L10-6002 | Layout | 5 | 5 | 26-Mar-14 | 01-Apr-14 | 65 |
| L14-6011 | PreRock Shafts | 2 | 2 | 26-Mar-14 | 27-Mar-14 | 70 |
| L08-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 27-Mar-14 | 31-Mar-14 | 72 |
| L08-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 27-Mar-14 | 27-Mar-14 | 71 |
| L09-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 27-Mar-14 | 27-Mar-14 | 66 |
| L14-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 27-Mar-14 | 27-Mar-14 | 70 |
| L15-6008 | Frame Shaft Walls | 3 | 3 | 27-Mar-14 | 31-Mar-14 | 63 |
| L16-8219 | HVAC Risers | 5 | 5 | 27-Mar-14 | 02-Apr-14 | 130 |
| L16-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 27-Mar-14 | 02-Apr-14 | 58 |
| L08-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 28-Mar-14 | 01-Apr-14 | 72 |
| L08-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 28-Mar-14 | 02-Apr-14 | 71 |
| L09-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 28-Mar-14 | 28-Mar-14 | 66 |
| L14-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 28-Mar-14 | 28-Mar-14 | 133 |
| L08-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 31-Mar-14 | 01-Apr-14 | 71 |
| L09-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 31-Mar-14 | 31-Mar-14 | 66 |
| L06-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 01-Apr-14 | 09-Apr-14 | 81 |
| L09-6012 | Fire Sprinkler Mains | 5 | 5 | 01-Apr-14 | 07-Apr-14 | 67 |
| L09-6014 | Set Tubs & Plumbing RI | 5 | 5 | 01-Apr-14 | 07-Apr-14 | 67 |
| L09-6016 | Electrical RI | 5 | 5 | 01-Apr-14 | 07-Apr-14 | 67 |
| L09-6018 | HVAC RI | 5 | 5 | 01-Apr-14 | 07-Apr-14 | 67 |
| L09-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 01-Apr-14 | 07-Apr-14 | 67 |
| L09-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 01-Apr-14 | 01-Apr-14 | 66 |
| L15-6009 | Inspect Shafts | 1 | 1 | 01-Apr-14 | 01-Apr-14 | 63 |
| L08-6024 | Inspections for GWB Cover | 1 | 1 | 02-Apr-14 | 02-Apr-14 | 71 |
| L09-6020 | Install Hollow Metal Frames | 3 | 3 | 02-Apr-14 | 04-Apr-14 | 71 |

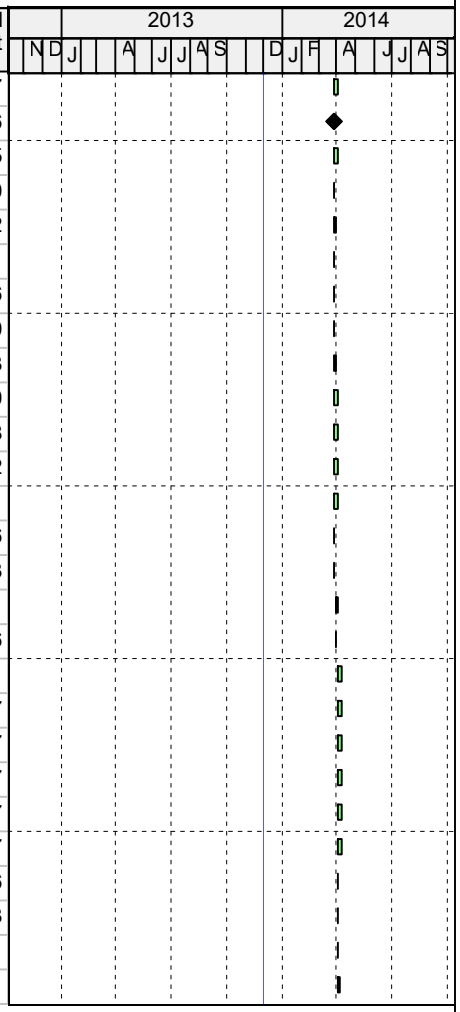



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6019 | Complete Top Out GWB | 2 | 2 | 02-Apr-14 | 03-Apr-14 | 67 |
| L09-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 02-Apr-14 | 02-Apr-14 | 66 |
| L10-6004 | CMU Wall/Clips | 3 | 3 | 02-Apr-14 | 04-Apr-14 | 128 |
| L10-6010 | Frame Walls | 5 | 5 | 02-Apr-14 | 08-Apr-14 | 62 |
| L10-6023 | Inspection of Exterior Framing | 0 | 0 | 02-Apr-14 | | 61 |
| L11-6002 | Layout | 5 | 5 | 02-Apr-14 | 08-Apr-14 | 20 |
| L15-6011 | PreRock Shafts | 2 | 2 | 02-Apr-14 | 03-Apr-14 | 65 |
| L09-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 03-Apr-14 | 07-Apr-14 | 67 |
| L09-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 03-Apr-14 | 03-Apr-14 | 66 |
| L10-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 03-Apr-14 | 03-Apr-14 | 61 |
| L15-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 03-Apr-14 | 03-Apr-14 | 65 |
| L16-6008 | Frame Shaft Walls | 3 | 3 | 03-Apr-14 | 07-Apr-14 | 58 |
| L09-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 04-Apr-14 | 08-Apr-14 | 67 |
| L09-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 04-Apr-14 | 09-Apr-14 | 66 |
| L10-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 04-Apr-14 | 04-Apr-14 | 61 |
| L15-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 04-Apr-14 | 04-Apr-14 | 128 |
| L09-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 07-Apr-14 | 08-Apr-14 | 66 |
| L10-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 07-Apr-14 | 07-Apr-14 | 61 |
| L07-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 08-Apr-14 | 16-Apr-14 | 76 |
| L10-6012 | Fire Sprinkler Mains | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 62 |
| L10-6014 | Set Tubs & Plumbing RI | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 62 |
| L10-6016 | Electrical RI | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 62 |
| L10-6018 | HVAC RI | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 62 |
| L10-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 62 |
| L10-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 08-Apr-14 | 08-Apr-14 | 61 |
| L16-6009 | Inspect Shafts | 1 | 1 | 08-Apr-14 | 08-Apr-14 | 58 |
| L09-6024 | Inspections for GWB Cover | 1 | 1 | 09-Apr-14 | 09-Apr-14 | 66 |

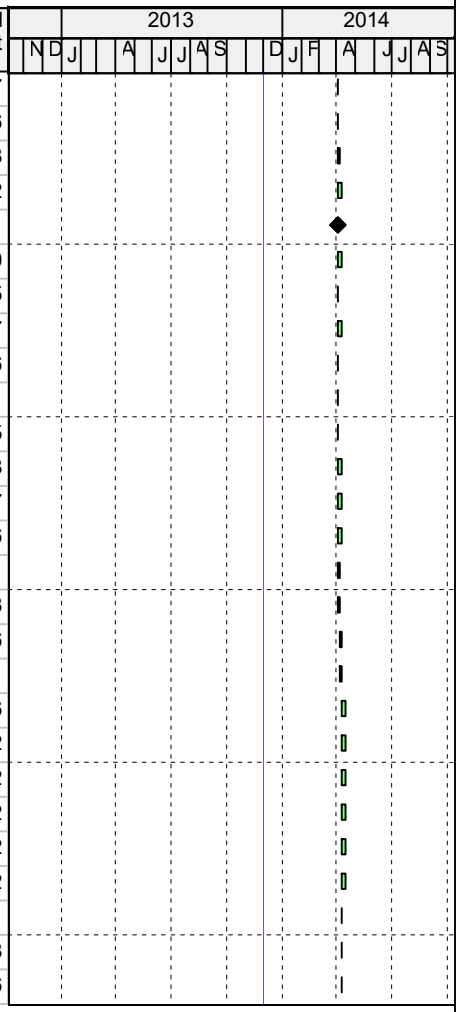



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-6020 | Install Hollow Metal Frames | 3 | 3 | 09-Apr-14 | 11-Apr-14 | 66 |
| L10-6019 | Complete Top Out GWB | 2 | 2 | 09-Apr-14 | 10-Apr-14 | 62 |
| L10-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 09-Apr-14 | 09-Apr-14 | 61 |
| L11-6004 | CMU Wall/Clips | 3 | 3 | 09-Apr-14 | 11-Apr-14 | 123 |
| L11-6010 | Frame Walls | 5 | 5 | 09-Apr-14 | 15-Apr-14 | 17 |
| L11-6023 | Inspection of Exterior Framing | 0 | 0 | 09-Apr-14 | | 16 |
| L16-6011 | PreRock Shafts | 2 | 2 | 09-Apr-14 | 10-Apr-14 | 60 |
| L10-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 10-Apr-14 | 14-Apr-14 | 62 |
| L10-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 10-Apr-14 | 10-Apr-14 | 61 |
| L11-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 10-Apr-14 | 10-Apr-14 | 16 |
| L16-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 10-Apr-14 | 10-Apr-14 | 60 |
| L17-8219 | HVAC Risers | 5 | 5 | 10-Apr-14 | 16-Apr-14 | 120 |
| L17-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 10-Apr-14 | 16-Apr-14 | 48 |
| L10-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 11-Apr-14 | 15-Apr-14 | 62 |
| L10-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 11-Apr-14 | 16-Apr-14 | 61 |
| L11-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 11-Apr-14 | 11-Apr-14 | 16 |
| L16-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 11-Apr-14 | 11-Apr-14 | 123 |
| L10-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 14-Apr-14 | 15-Apr-14 | 61 |
| L11-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 14-Apr-14 | 14-Apr-14 | 16 |
| L08-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 15-Apr-14 | 23-Apr-14 | 71 |
| L11-6012 | Fire Sprinkler Mains | 5 | 5 | 15-Apr-14 | 21-Apr-14 | 17 |
| L11-6014 | Set Tubs & Plumbing RI | 5 | 5 | 15-Apr-14 | 21-Apr-14 | 17 |
| L11-6016 | Electrical RI | 5 | 5 | 15-Apr-14 | 21-Apr-14 | 17 |
| L11-6018 | HVAC RI | 5 | 5 | 15-Apr-14 | 21-Apr-14 | 17 |
| L11-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 15-Apr-14 | 21-Apr-14 | 17 |
| L11-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 15-Apr-14 | 15-Apr-14 | 16 |
| L10-6024 | Inspections for GWB Cover | 1 | 1 | 16-Apr-14 | 16-Apr-14 | 61 |

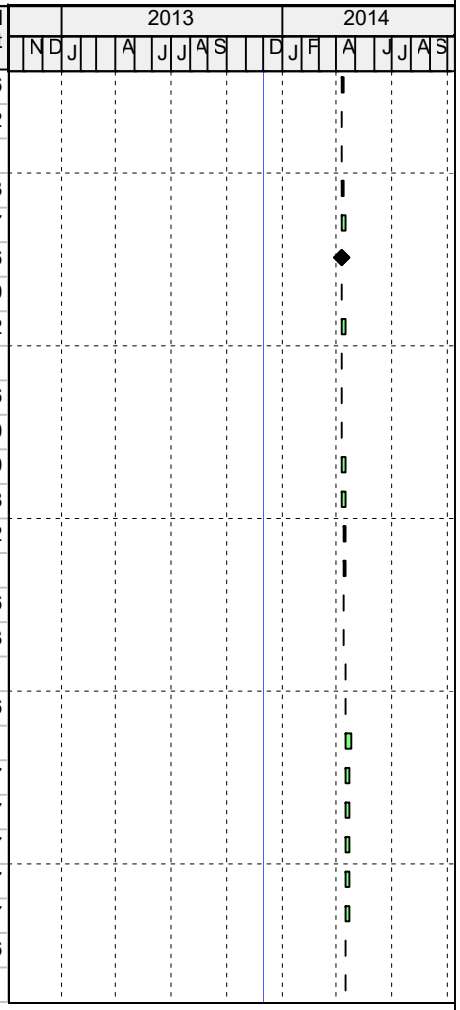



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6020 | Install Hollow Metal Frames | 3 | 3 | 16-Apr-14 | 18-Apr-14 | 21 |
| L11-6019 | Complete Top Out GWB | 2 | 2 | 16-Apr-14 | 17-Apr-14 | 17 |
| L11-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 16-Apr-14 | 16-Apr-14 | 16 |
| L12-6002 | Layout | 5 | 5 | 16-Apr-14 | 22-Apr-14 | 50 |
| L14-6002 | Layout | 5 | 5 | 16-Apr-14 | 22-Apr-14 | 50 |
| L11-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 17-Apr-14 | 21-Apr-14 | 17 |
| L11-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 17-Apr-14 | 17-Apr-14 | 16 |
| L17-6008 | Frame Shaft Walls | 3 | 3 | 17-Apr-14 | 21-Apr-14 | 48 |
| L11-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 18-Apr-14 | 22-Apr-14 | 17 |
| L11-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 18-Apr-14 | 23-Apr-14 | 16 |
| L15-6002 | Layout | 5 | 5 | 18-Apr-14 | 24-Apr-14 | 48 |
| L11-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 21-Apr-14 | 22-Apr-14 | 16 |
| L09-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 22-Apr-14 | 30-Apr-14 | 66 |
| L16-6002 | Layout | 5 | 5 | 22-Apr-14 | 28-Apr-14 | 46 |
| L17-6009 | Inspect Shafts | 1 | 1 | 22-Apr-14 | 22-Apr-14 | 48 |
| L11-6024 | Inspections for GWB Cover | 1 | 1 | 23-Apr-14 | 23-Apr-14 | 16 |
| L12-6004 | CMU Wall/Clips | 3 | 3 | 23-Apr-14 | 25-Apr-14 | 113 |
| L12-6010 | Frame Walls | 5 | 5 | 23-Apr-14 | 29-Apr-14 | 47 |
| L12-6023 | Inspection of Exterior Framing | 0 | 0 | 23-Apr-14 | | 46 |
| L14-6004 | CMU Wall/Clips | 3 | 3 | 23-Apr-14 | 25-Apr-14 | 113 |
| L17-6011 | PreRock Shafts | 2 | 2 | 23-Apr-14 | 24-Apr-14 | 50 |
| L12-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 1 | 24-Apr-14 | 24-Apr-14 | 46 |
| L17-6002 | Layout | 5 | 5 | 24-Apr-14 | 30-Apr-14 | 38 |
| L17-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 24-Apr-14 | 24-Apr-14 | 50 |
| L12-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 25-Apr-14 | 25-Apr-14 | 46 |
| L15-6004 | CMU Wall/Clips | 3 | 3 | 25-Apr-14 | 29-Apr-14 | 111 |
| L17-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 25-Apr-14 | 25-Apr-14 | 113 |

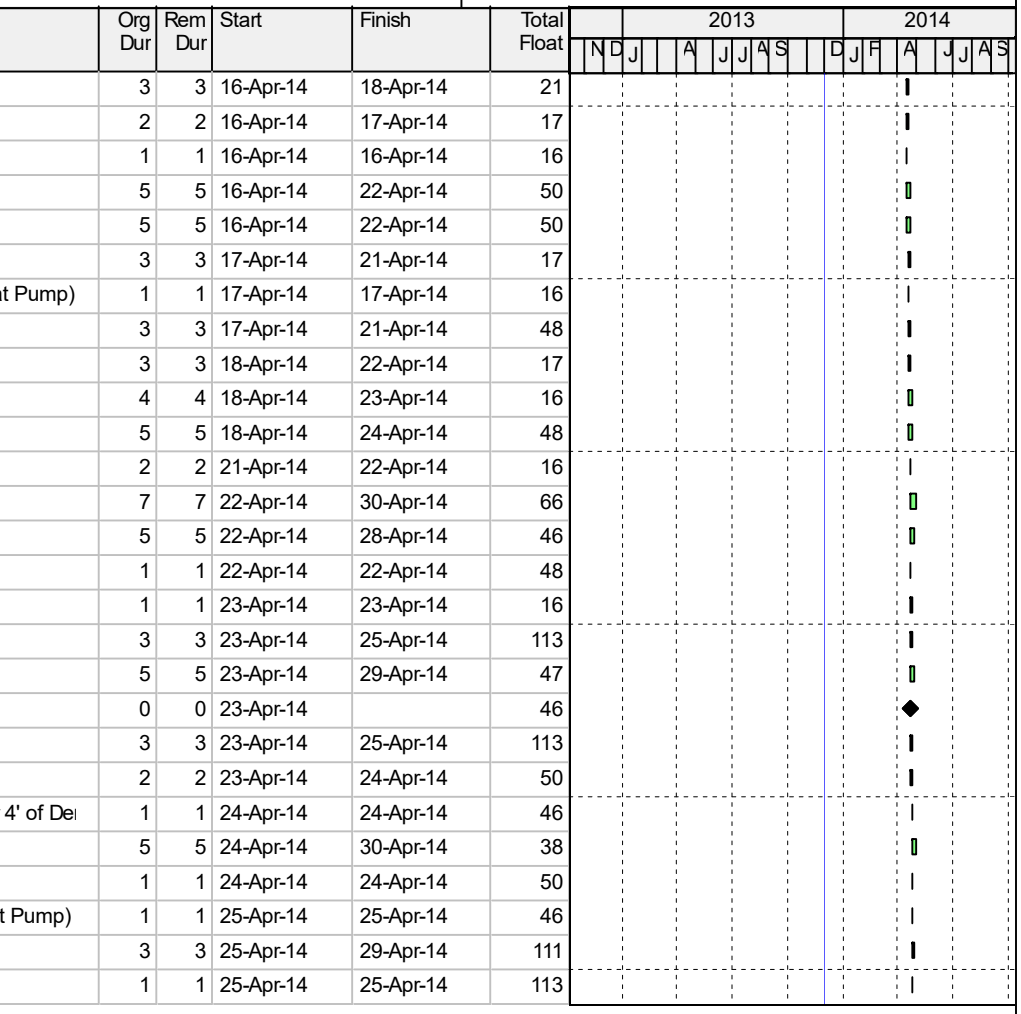



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 28-Apr-14 | 28-Apr-14 | 46 |
| L10-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 29-Apr-14 | 07-May-14 | 61 |
| L12-6012 | Fire Sprinkler Mains | 5 | 5 | 29-Apr-14 | 05-May-14 | 47 |
| L12-6014 | Set Tubs & Plumbing RI | 5 | 5 | 29-Apr-14 | 05-May-14 | 47 |
| L12-6016 | Electrical RI | 5 | 5 | 29-Apr-14 | 05-May-14 | 47 |
| L12-6018 | HVAC RI | 5 | 5 | 29-Apr-14 | 05-May-14 | 47 |
| L12-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 29-Apr-14 | 05-May-14 | 47 |
| L12-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 29-Apr-14 | 29-Apr-14 | 46 |
| L16-6004 | CMU Wall/Clips | 3 | 3 | 29-Apr-14 | 01-May-14 | 109 |
| L12-6020 | Install Hollow Metal Frames | 3 | 3 | 30-Apr-14 | 02-May-14 | 51 |
| L12-6019 | Complete Top Out GWB | 2 | 2 | 30-Apr-14 | 01-May-14 | 47 |
| L12-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 30-Apr-14 | 30-Apr-14 | 46 |
| L14-6010 | Frame Walls | 5 | 5 | 30-Apr-14 | 06-May-14 | 42 |
| L14-6023 | Inspection of Exterior Framing | 0 | 0 | 30-Apr-14 | | 41 |
| L12-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 01-May-14 | 05-May-14 | 47 |
| L12-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 01-May-14 | 01-May-14 | 46 |
| L14-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 01-May-14 | 01-May-14 | 41 |
| L17-6004 | CMU Wall/Clips | 3 | 3 | 01-May-14 | 05-May-14 | 107 |
| L12-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 02-May-14 | 06-May-14 | 47 |
| L12-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 02-May-14 | 07-May-14 | 46 |
| L14-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 02-May-14 | 02-May-14 | 41 |
| L12-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 05-May-14 | 06-May-14 | 46 |
| L14-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 05-May-14 | 05-May-14 | 41 |
| L11-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 06-May-14 | 14-May-14 | 16 |
| L14-6012 | Fire Sprinkler Mains | 5 | 5 | 06-May-14 | 12-May-14 | 42 |
| L14-6014 | Set Tubs & Plumbing RI | 5 | 5 | 06-May-14 | 12-May-14 | 42 |
| L14-6016 | Electrical RI | 5 | 5 | 06-May-14 | 12-May-14 | 42 |

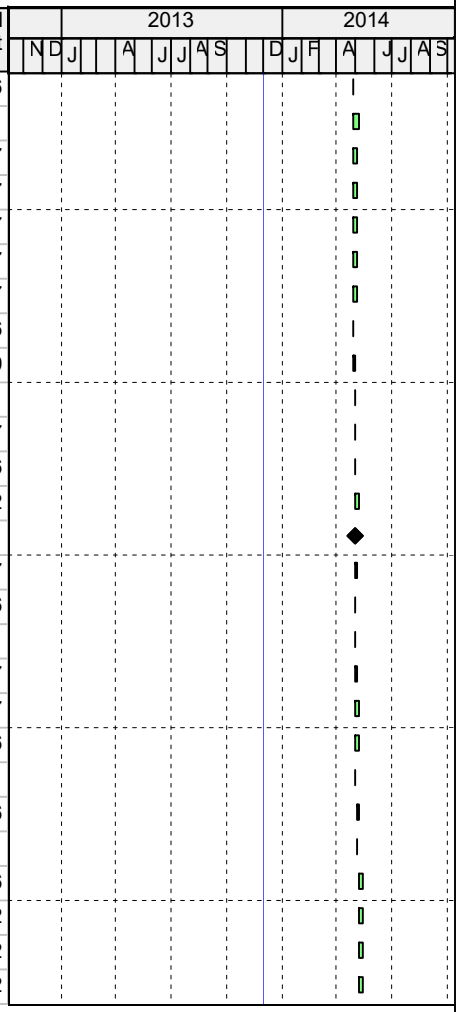



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6018 | HVAC RI | 5 | 5 | 06-May-14 | 12-May-14 | 42 |
| L14-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 06-May-14 | 12-May-14 | 42 |
| L14-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 06-May-14 | 06-May-14 | 41 |
| L12-6024 | Inspections for GWB Cover | 1 | 1 | 07-May-14 | 07-May-14 | 46 |
| L14-6020 | Install Hollow Metal Frames | 3 | 3 | 07-May-14 | 09-May-14 | 46 |
| L14-6019 | Complete Top Out GWB | 2 | 2 | 07-May-14 | 08-May-14 | 42 |
| L14-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 07-May-14 | 07-May-14 | 41 |
| L15-6010 | Frame Walls | 5 | 5 | 07-May-14 | 13-May-14 | 37 |
| L15-6023 | Inspection of Exterior Framing | 0 | 0 | 07-May-14 | | 36 |
| L14-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 08-May-14 | 12-May-14 | 42 |
| L14-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 08-May-14 | 08-May-14 | 41 |
| L15-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 1 | 08-May-14 | 08-May-14 | 36 |
| L14-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 09-May-14 | 13-May-14 | 42 |
| L14-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 09-May-14 | 14-May-14 | 41 |
| L15-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 09-May-14 | 09-May-14 | 36 |
| L14-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 12-May-14 | 13-May-14 | 41 |
| L15-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 12-May-14 | 12-May-14 | 36 |
| L15-6012 | Fire Sprinkler Mains | 5 | 5 | 13-May-14 | 19-May-14 | 37 |
| L15-6014 | Set Tubs & Plumbing RI | 5 | 5 | 13-May-14 | 19-May-14 | 37 |
| L15-6016 | Electrical RI | 5 | 5 | 13-May-14 | 19-May-14 | 37 |
| L15-6018 | HVAC RI | 5 | 5 | 13-May-14 | 19-May-14 | 37 |
| L15-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 13-May-14 | 19-May-14 | 37 |
| L15-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 13-May-14 | 13-May-14 | 36 |
| L14-6024 | Inspections for GWB Cover | 1 | 1 | 14-May-14 | 14-May-14 | 41 |
| L15-6020 | Install Hollow Metal Frames | 3 | 3 | 14-May-14 | 16-May-14 | 41 |
| L15-6019 | Complete Top Out GWB | 2 | 2 | 14-May-14 | 15-May-14 | 37 |
| L15-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 14-May-14 | 14-May-14 | 36 |

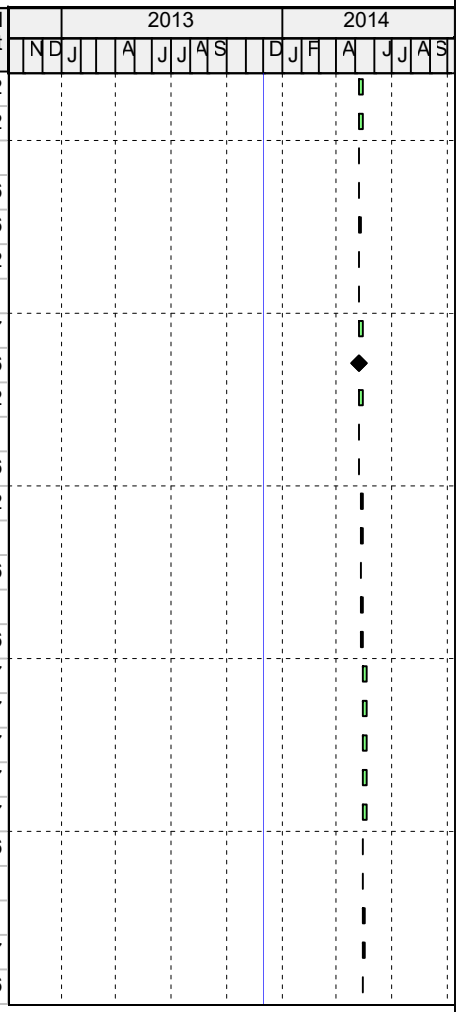



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6010 | Frame Walls | 5 | 5 | 14-May-14 | 20-May-14 | 32 |
| L16-6023 | Inspection of Exterior Framing | 0 | 0 | 14-May-14 | | 31 |
| L15-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 15-May-14 | 19-May-14 | 37 |
| L15-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 15-May-14 | 15-May-14 | 36 |
| L16-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 15-May-14 | 15-May-14 | 31 |
| L15-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 16-May-14 | 20-May-14 | 37 |
| L15-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 16-May-14 | 21-May-14 | 36 |
| L16-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 16-May-14 | 16-May-14 | 31 |
| L15-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 19-May-14 | 20-May-14 | 36 |
| L16-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 19-May-14 | 19-May-14 | 31 |
| L12-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 20-May-14 | 29-May-14 | 46 |
| L16-6012 | Fire Sprinkler Mains | 5 | 5 | 20-May-14 | 27-May-14 | 32 |
| L16-6014 | Set Tubs & Plumbing RI | 5 | 5 | 20-May-14 | 27-May-14 | 32 |
| L16-6016 | Electrical RI | 5 | 5 | 20-May-14 | 27-May-14 | 32 |
| L16-6018 | HVAC RI | 5 | 5 | 20-May-14 | 27-May-14 | 32 |
| L16-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 20-May-14 | 27-May-14 | 32 |
| L16-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 20-May-14 | 20-May-14 | 31 |
| L15-6024 | Inspections for GWB Cover | 1 | 1 | 21-May-14 | 21-May-14 | 36 |
| L16-6020 | Install Hollow Metal Frames | 3 | 3 | 21-May-14 | 23-May-14 | 36 |
| L16-6019 | Complete Top Out GWB | 2 | 2 | 21-May-14 | 22-May-14 | 32 |
| L16-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 21-May-14 | 21-May-14 | 31 |
| L17-6010 | Frame Walls | 5 | 5 | 21-May-14 | 28-May-14 | 27 |
| L17-6023 | Inspection of Exterior Framing | 0 | 0 | 21-May-14 | | 26 |
| L16-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 22-May-14 | 27-May-14 | 32 |
| L16-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 22-May-14 | 22-May-14 | 31 |
| L17-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 22-May-14 | 22-May-14 | 26 |
| L16-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 23-May-14 | 28-May-14 | 32 |

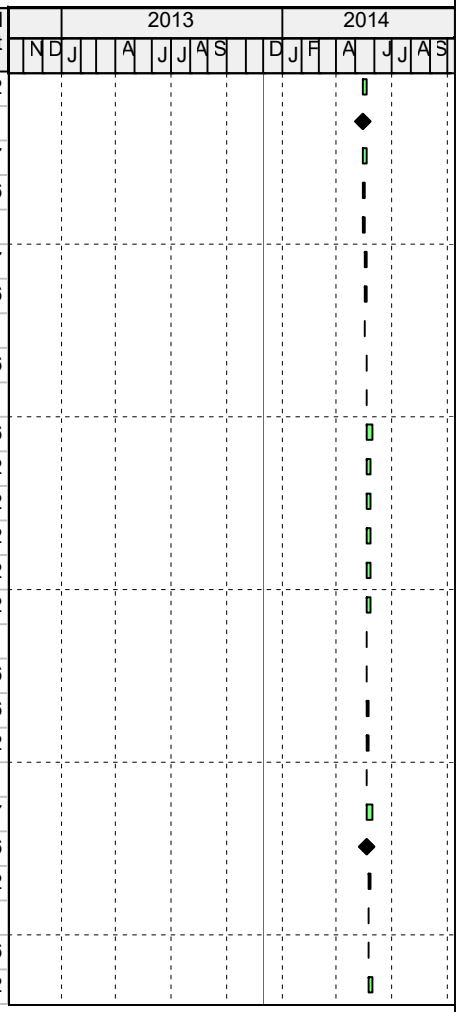


Actual Work | Remaining Work | Critical Remai... | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 23-May-14 | 29-May-14 | 31 |
| L17-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 23-May-14 | 23-May-14 | 26 |
| L16-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 27-May-14 | 28-May-14 | 31 |
| L17-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 27-May-14 | 27-May-14 | 26 |
| L14-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 28-May-14 | 05-Jun-14 | 41 |
| L17-6012 | Fire Sprinkler Mains | 5 | 5 | 28-May-14 | 03-Jun-14 | 27 |
| L17-6014 | Set Tubs & Plumbing RI | 5 | 5 | 28-May-14 | 03-Jun-14 | 27 |
| L17-6016 | Electrical RI | 5 | 5 | 28-May-14 | 03-Jun-14 | 27 |
| L17-6018 | HVAC RI | 5 | 5 | 28-May-14 | 03-Jun-14 | 27 |
| L17-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 28-May-14 | 03-Jun-14 | 27 |
| L17-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 28-May-14 | 28-May-14 | 26 |
| L16-6024 | Inspections for GWB Cover | 1 | 1 | 29-May-14 | 29-May-14 | 31 |
| L17-6020 | Install Hollow Metal Frames | 3 | 3 | 29-May-14 | 02-Jun-14 | 31 |
| L17-6019 | Complete Top Out GWB | 2 | 2 | 29-May-14 | 30-May-14 | 27 |
| L17-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 29-May-14 | 29-May-14 | 26 |
| L17-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 30-May-14 | 03-Jun-14 | 27 |
| L17-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 30-May-14 | 30-May-14 | 26 |
| L17-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 02-Jun-14 | 04-Jun-14 | 27 |
| L17-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 02-Jun-14 | 05-Jun-14 | 26 |
| L17-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 03-Jun-14 | 04-Jun-14 | 26 |
| L15-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 04-Jun-14 | 12-Jun-14 | 36 |
| L17-6024 | Inspections for GWB Cover | 1 | 1 | 05-Jun-14 | 05-Jun-14 | 26 |
| L16-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 11-Jun-14 | 19-Jun-14 | 31 |
| L17-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 18-Jun-14 | 26-Jun-14 | 26 |
| **Mechanical Penthouse** | | | | | | |
| PH-6002 | PH - Layout | 1 | 1 | 01-May-14 | 01-May-14 | 38 |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 5 | 02-May-14 | 08-May-14 | 49 |

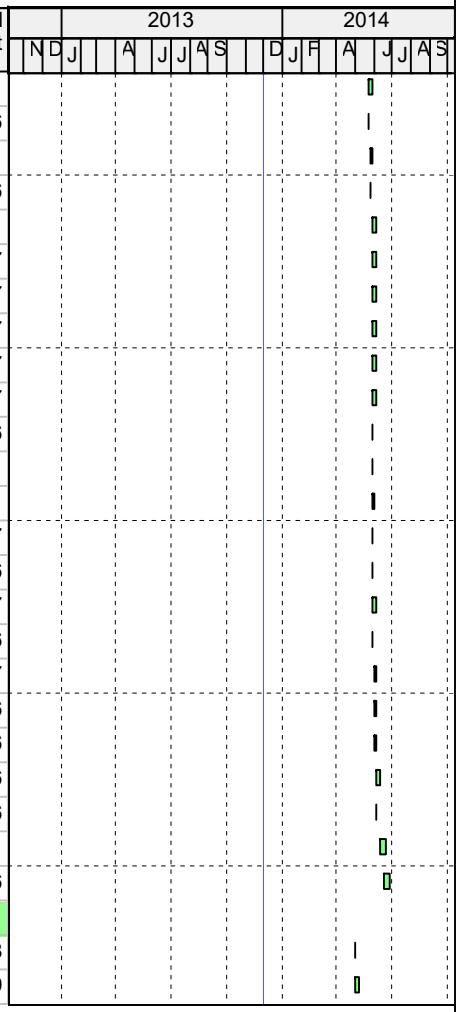



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-6006 | PH - Ext Wall Framing - (Incldg Roof Parapet) | 10 | 10 | 02-May-14 | 15-May-14 | 38 |
| PH-6008 | PH - Int Wall Framing | 3 | 3 | 16-May-14 | 20-May-14 | 38 |
| PH-6012 | PH - Fire Sprinkler Rl | 8 | 8 | 21-May-14 | 02-Jun-14 | 45 |
| PH-6014 | PH - Plumbing Rl | 12 | 12 | 21-May-14 | 06-Jun-14 | 41 |
| PH-6016 | PH - Electrical Rl | 12 | 12 | 21-May-14 | 06-Jun-14 | 41 |
| PH-6018 | PH - HVAC Rl | 15 | 15 | 21-May-14 | 11-Jun-14 | 38 |
| PH-6020 | PH - H Mtl Frames | 2 | 2 | 21-May-14 | 22-May-14 | 56 |
| PH-6022 | PH - Fire Alarm / Elec Specialties Rl | 5 | 5 | 21-May-14 | 28-May-14 | 69 |
| PH-6024 | PH - Inspections | 2 | 2 | 12-Jun-14 | 13-Jun-14 | 38 |
| **Finishes** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL4-8100 | LL4 - Insulation | 1 | 1 | 06-Mar-14 | 06-Mar-14 | 86 |
| LL4-8102 | LL4 - GWB Hang / Tape / Finish - (Including Commor | 5 | 5 | 07-Mar-14 | 13-Mar-14 | 86 |
| LL4-8104 | LL4 - Int Painting | 3 | 3 | 11-Mar-14 | 13-Mar-14 | 109 |
| LL4-8110 | LL4 - HVAC Trim / Finish | 6 | 6 | 14-Mar-14 | 21-Mar-14 | 110 |
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 5 | 5 | 14-Mar-14 | 20-Mar-14 | 111 |
| LL4-8114 | LL4 - Striping / Signage | 3 | 3 | 14-Mar-14 | 18-Mar-14 | 122 |
| LL4-8118 | LL4 - Elec Specialties Trim / Finish | 4 | 4 | 14-Mar-14 | 19-Mar-14 | 112 |
| LL4-8122 | LL4 - Plumbing Trim / Finish | 5 | 5 | 24-Mar-14 | 28-Mar-14 | 109 |
| LL4-8108 | LL4 - Elec Trim / Finish | 6 | 6 | 27-Mar-14 | 03-Apr-14 | 101 |
| LL4-6026 | LL4 - Pull Wire | 6 | 6 | 27-Mar-14 | 03-Apr-14 | 101 |
| LL4-8124 | LL4 - Flooring | 3 | 3 | 04-Apr-14 | 08-Apr-14 | 101 |
| LL4-8126 | LL4 - Doors & Hardware | 3 | 3 | 07-Apr-14 | 09-Apr-14 | 101 |
| LL4-8130 | LL4 - Substantially Complete | 0 | 0 | | 09-Apr-14 | 101 |
| LL4-8132 | LL4 - Contractor Pre-Punchlist | 5 | 5 | 10-Apr-14 | 16-Apr-14 | 104 |

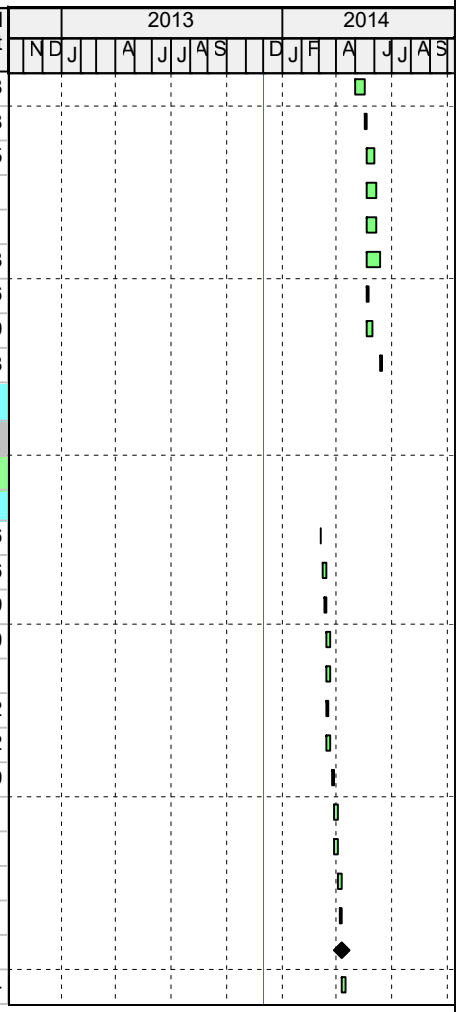



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8134 | LL4 - Pre-Clean | 5 | 5 | 10-Apr-14 | 16-Apr-14 | 101 |
| LL4-8208 | LL4 - Final Clean | 3 | 3 | 17-Apr-14 | 21-Apr-14 | 101 |
| LL4-8210 | LL4 - Owner Walk / Create Punchlist | 1 | 1 | 22-Apr-14 | 22-Apr-14 | 101 |
| LL4-8212 | LL4 - Final Punchlist | 5 | 5 | 23-Apr-14 | 29-Apr-14 | 101 |
| LL4-8214 | LL4 - Floor Complete | 0 | 0 | | 29-Apr-14 | 101 |
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL3-8100 | LL3 - Insulation | 1 | 1 | 27-Mar-14 | 27-Mar-14 | 72 |
| LL3-8102 | LL3 - GWB Hang / Tape / Finish - (Including Commor | 5 | 5 | 28-Mar-14 | 03-Apr-14 | 74 |
| LL3-6026 | LL3 - Pull Wire | 6 | 6 | 28-Mar-14 | 04-Apr-14 | 105 |
| LL3-8104 | LL3 - Int Painting | 3 | 3 | 01-Apr-14 | 03-Apr-14 | 99 |
| LL3-8108 | LL3 - Elec Trim / Finish | 6 | 6 | 04-Apr-14 | 11-Apr-14 | 100 |
| LL3-8110 | LL3 - HVAC Trim / Finish | 6 | 6 | 04-Apr-14 | 11-Apr-14 | 100 |
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 5 | 5 | 04-Apr-14 | 10-Apr-14 | 101 |
| LL3-8114 | LL3 - Striping / Signage | 3 | 3 | 04-Apr-14 | 08-Apr-14 | 112 |
| LL3-8118 | LL3 - Elec Specialties Trim / Finish | 4 | 4 | 04-Apr-14 | 09-Apr-14 | 102 |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 5 | 5 | 14-Apr-14 | 18-Apr-14 | 99 |
| LL3-8124 | LL3 - Flooring | 3 | 3 | 14-Apr-14 | 16-Apr-14 | 100 |
| LL3-8126 | LL3 - Doors & Hardware | 3 | 3 | 15-Apr-14 | 17-Apr-14 | 100 |
| LL3-8130 | LL3 - Substantially Complete | 0 | 0 | | 18-Apr-14 | 99 |
| LL3-8132 | LL3 - Contractor Pre-Punchlist | 5 | 5 | 21-Apr-14 | 25-Apr-14 | 102 |
| LL3-8134 | LL3 - Pre-Clean | 5 | 5 | 21-Apr-14 | 25-Apr-14 | 99 |
| LL3-8208 | LL3 - Final Clean | 3 | 3 | 28-Apr-14 | 30-Apr-14 | 99 |
| LL3-8210 | LL3 - Owner Walk / Create Punchlist | 1 | 1 | 01-May-14 | 01-May-14 | 99 |
| LL3-8212 | LL3 - Final Punchlist | 5 | 5 | 02-May-14 | 08-May-14 | 99 |
| LL3-8214 | LL3 - Floor Complete | 0 | 0 | | 08-May-14 | 99 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |

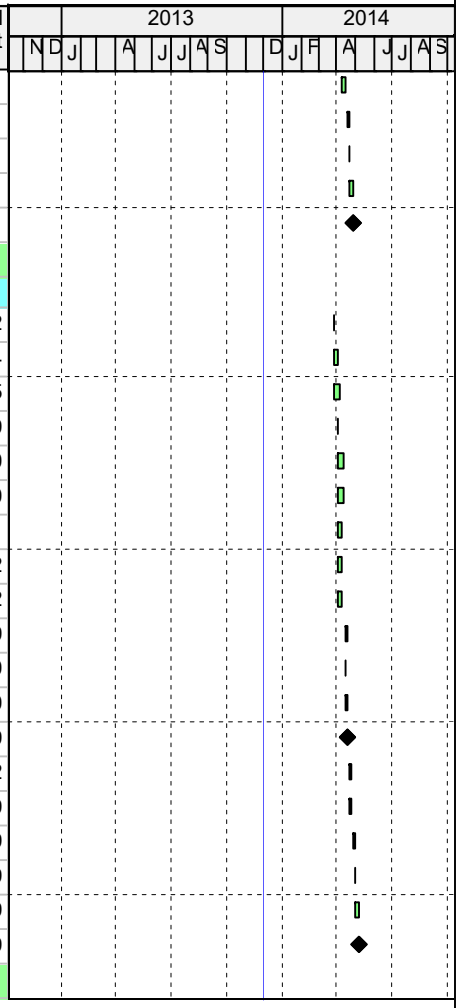



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Corridors / Common / Public Areas** | | | | | | |
| LL2-8100 | LL2 - Insulation | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 4 |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish - (Including Commor | 15 | 15 | 11-Jul-14 | 31-Jul-14 | 4 |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 10 | 10 | 11-Jul-14 | 24-Jul-14 | 32 |
| LL2-6026 | LL2 - Pull Wire | 15 | 15 | 11-Jul-14 | 31-Jul-14 | 26 |
| LL2-8128 | LL2 - Entry Gates | 3 | 3 | 25-Jul-14 | 29-Jul-14 | 32 |
| LL2-8104 | LL2 - Int Painting | 5 | 5 | 29-Jul-14 | 04-Aug-14 | 4 |
| LL2-8136 | LL2 - Chainlink Fencing / Gate @ Recycling | 2 | 2 | 30-Jul-14 | 31-Jul-14 | 32 |
| LL2-8120 | LL2 - Steel Pipe Guardrails | 6 | 6 | 01-Aug-14 | 08-Aug-14 | 26 |
| LL2-8108 | LL2 - Elec Trim / Finish | 20 | 20 | 05-Aug-14 | 02-Sep-14 | 4 |
| LL2-8110 | LL2 - HVAC Trim / Finish | 12 | 12 | 05-Aug-14 | 20-Aug-14 | 12 |
| LL2-8112 | LL2 - Fire Sprinkler Trim / Finish | 8 | 8 | 05-Aug-14 | 14-Aug-14 | 16 |
| LL2-8114 | LL2 - Striping / Signage | 3 | 3 | 05-Aug-14 | 07-Aug-14 | 32 |
| LL2-8116 | LL2 - Finish Carpentry / Millwork | 2 | 2 | 05-Aug-14 | 06-Aug-14 | 21 |
| LL2-8118 | LL2 - Elec Specialties Trim / Finish | 4 | 4 | 05-Aug-14 | 08-Aug-14 | 20 |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 9 | 9 | 05-Aug-14 | 15-Aug-14 | 21 |
| LL2-8122 | LL2 - Plumbing Trim / Finish | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 21 |
| LL2-8126 | LL2 - Doors & Hardware | 7 | 7 | 02-Sep-14 | 10-Sep-14 | 4 |
| LL2-8124 | LL2 - Flooring | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 4 |
| LL2-8130 | LL2 - Substantially Complete | 0 | 0 | | 10-Sep-14 | 4 |
| LL2-8132 | LL2 - Contractor Pre-Punchlist | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 7 |
| LL2-8134 | LL2 - Pre-Clean | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 4 |
| LL2-8208 | LL2 - Final Clean | 3 | 3 | 18-Sep-14 | 22-Sep-14 | 4 |
| LL2-8210 | LL2 - Owner Walk / Create Punchlist | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 4 |
| LL2-8212 | LL2 - Final Punchlist | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 4 |
| LL2-8214 | LL2 - Floor Complete | 0 | 0 | | 30-Sep-14 | 4 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |

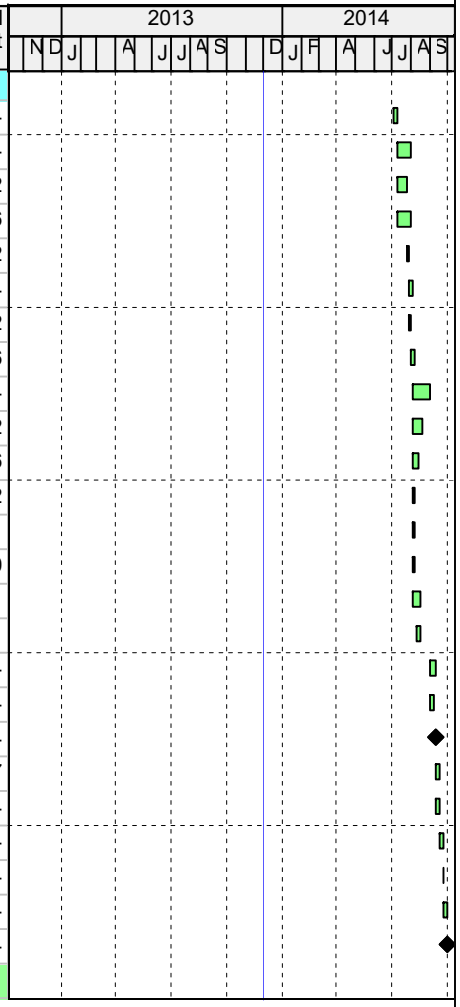



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1-8100 | LL1 - Insulation | 5 | 5 | 16-Apr-14 | 22-Apr-14 | 0 |
| LL1-8102 | LL1 - GWB Hang / Tape / Finish - (Including Commor | 25 | 25 | 23-Apr-14 | 28-May-14 | 0 |
| LL1-6026 | LL1 - Pull Wire | 10 | 10 | 23-Apr-14 | 06-May-14 | 47 |
| LL1-8104 | LL1 - Int Painting | 15 | 15 | 23-May-14 | 13-Jun-14 | 0 |
| LL1-8106 | LL1 - Wallcoverings | 6 | 6 | 28-May-14 | 04-Jun-14 | 27 |
| LL1-8116 | LL1 - Finish Carpentry / Millwork | 20 | 20 | 02-Jun-14 | 27-Jun-14 | 10 |
| LL1-8120 | LL1 - Ceramic Tile / Counter Tops | 12 | 12 | 04-Jun-14 | 19-Jun-14 | 16 |
| LL1-8122 | LL1 - Plumbing Trim / Finish | 10 | 10 | 06-Jun-14 | 19-Jun-14 | 22 |
| LL1-8112 | LL1 - Fire Sprinkler Trim / Finish | 8 | 8 | 16-Jun-14 | 25-Jun-14 | 12 |
| LL1-8118 | LL1 - Elec Specialties Trim / Finish | 10 | 10 | 16-Jun-14 | 27-Jun-14 | 10 |
| LL1-8114 | LL1 - T-Bar Grid Ceiling | 8 | 8 | 16-Jun-14 | 25-Jun-14 | 0 |
| LL1-8128 | LL1 - Bath Specialties | 3 | 3 | 20-Jun-14 | 24-Jun-14 | 22 |
| LL1-8136 | LL1 - Toilet Partitions | 5 | 5 | 20-Jun-14 | 26-Jun-14 | 20 |
| LL1-8108 | LL1 - Elec Trim / Finish | 12 | 12 | 26-Jun-14 | 14-Jul-14 | 0 |
| LL1-8110 | LL1 - HVAC Trim / Finish | 10 | 10 | 26-Jun-14 | 10-Jul-14 | 2 |
| LL1-8138 | LL1 - Epoxy Flooring @ Food Prep | 7 | 7 | 30-Jun-14 | 09-Jul-14 | 12 |
| LL1-8142 | LL1 - Folding Partitions @ Meeting Rooms | 8 | 8 | 30-Jun-14 | 10-Jul-14 | 11 |
| LL1-8124 | LL1 - Flooring @ Meeting Rooms | 8 | 8 | 15-Jul-14 | 24-Jul-14 | 0 |
| LL1-8140 | LL1 - Acoustical Ceiling Tile | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 4 |
| LL1-8126 | LL1 - Doors & Hardware | 8 | 8 | 16-Jul-14 | 25-Jul-14 | 0 |
| LL1-8130 | LL1 - Meeting Rooms / Food Prep Substantially Com | 0 | 0 | | 25-Jul-14 | 0 |
| LL1-8132 | LL1 - Contractor Pre-Punchlist | 10 | 10 | 28-Jul-14 | 08-Aug-14 | 29 |
| LL1-8134 | LL1 - Pre-Clean | 8 | 8 | 28-Jul-14 | 06-Aug-14 | 26 |
| **Corridors / Common / Public Areas** | | | | | | |
| LL1-8200 | LL1 - Final Paint @ Common / Public Areas | 6 | 6 | 28-Jul-14 | 04-Aug-14 | 0 |
| LL1-8202 | LL1 - Elec Trim / Finish @ Common / Public Areas | 10 | 10 | 05-Aug-14 | 18-Aug-14 | 4 |

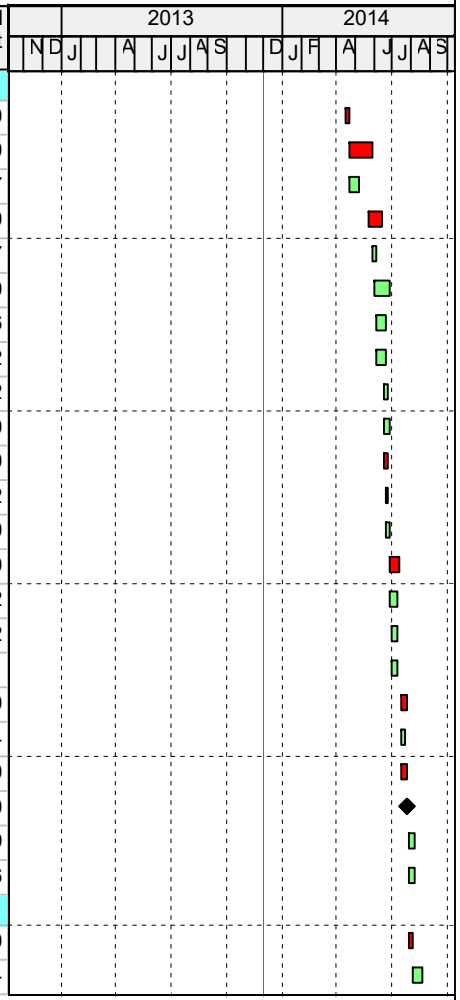



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-8204 | LL1 - Mech Trim / Finish @ Common / Public Areas | 12 | 12 | 05-Aug-14 | 16-Aug-14 | 0 |
| LL1-8206 | LL1 - Flooring @ Common / Public Areas | 6 | 6 | 18-Aug-14 | 25-Aug-14 | 13 |
| LL1-8208 | LL1 - Final Clean | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 13 |
| LL1-8210 | LL1 - Owner Walk / Create Punchlist | 1 | 1 | 03-Sep-14 | 03-Sep-14 | 13 |
| LL1-8212 | LL1 - Final Punchlist | 10 | 10 | 04-Sep-14 | 17-Sep-14 | 13 |
| LL1-8214 | LL1 - Floor Complete | 0 | 0 | | 17-Sep-14 | 13 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| L01-8200 | L1 - Final Paint @ Common / Public Areas | 6 | 6 | 05-Aug-14 | 12-Aug-14 | 14 |
| L01-8206 | L1 - Flooring @ Common / Public Areas | 10 | 10 | 11-Aug-14 | 22-Aug-14 | 14 |
| L01-8202 | L1 - Elec Trim / Finish @ Common / Public Areas | 8 | 8 | 13-Aug-14 | 22-Aug-14 | 15 |
| L01-8204 | L1 - Mech Trim / Finish @ Common / Public Areas | 8 | 8 | 13-Aug-14 | 22-Aug-14 | 14 |
| L01-8208 | L1 - Final Clean | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 14 |
| L01-8216 | L1 - Entry Mats | 2 | 2 | 25-Aug-14 | 26-Aug-14 | 17 |
| L01-8210 | L1 - Owner Walk / Create Punchlist | 1 | 1 | 02-Sep-14 | 02-Sep-14 | 14 |
| L01-8212 | L1 - Final Punchlist | 10 | 10 | 03-Sep-14 | 16-Sep-14 | 14 |
| L01-8214 | L1 - Floor Complete | 0 | 0 | | 16-Sep-14 | 14 |
| **Main Ballrooms / Meeting Rooms / Kitchen / Lobby / Dining** | | | | | | |
| L01-8100 | L1 - Insulation | 5 | 5 | 20-May-14 | 27-May-14 | 14 |
| L01-6026 | L1 - Pull Wire | 10 | 10 | 20-May-14 | 03-Jun-14 | 48 |
| L01-8102 | L1 - GWB Hang / Tape / Finish - (Including Common / | 20 | 20 | 28-May-14 | 24-Jun-14 | 14 |
| L01-8104 | L1 - Int Painting | 10 | 10 | 20-Jun-14 | 03-Jul-14 | 14 |
| L01-8106 | L1 - Wallcoverings | 6 | 6 | 24-Jun-14 | 01-Jul-14 | 28 |
| L01-8116 | L1 - Finish Carpentry / Millwork | 14 | 14 | 27-Jun-14 | 17-Jul-14 | 17 |
| L01-8120 | L1 - Ceramic Tile / Counter Tops @ Restrooms | 12 | 12 | 01-Jul-14 | 17-Jul-14 | 17 |
| L01-8122 | L1 - Plumbing Trim / Finish | 10 | 10 | 03-Jul-14 | 17-Jul-14 | 23 |
| L01-8108 | L1 - Elec Trim / Finish | 12 | 12 | 07-Jul-14 | 22-Jul-14 | 14 |

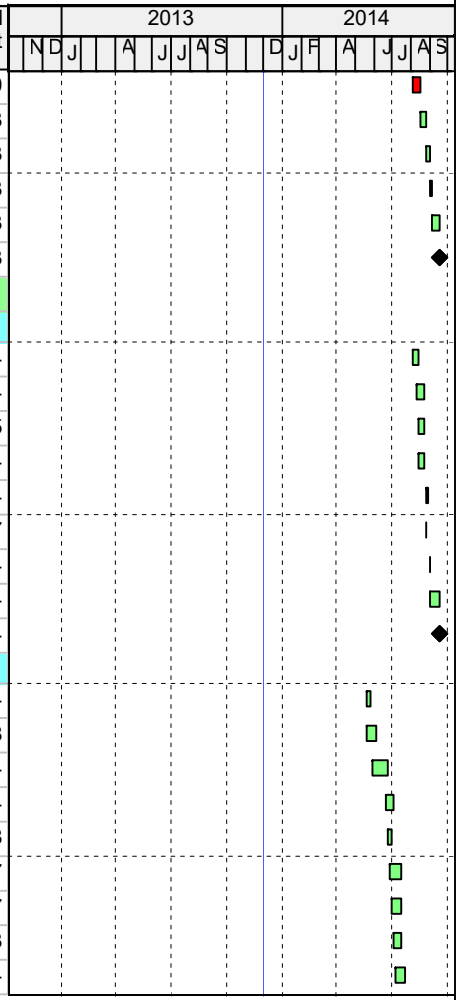


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L01-8110 | L1 - HVAC Trim / Finish | 10 | 10 | 07-Jul-14 | 18-Jul-14 | 16 |
| L01-8112 | L1 - Fire Sprinkler Trim / Finish | 8 | 8 | 07-Jul-14 | 16-Jul-14 | 18 |
| L01-8118 | L1 - Elec Specialties Trim / Finish | 6 | 6 | 07-Jul-14 | 14-Jul-14 | 20 |
| L01-8136 | L1 - Casework / Front Desk | 10 | 10 | 07-Jul-14 | 18-Jul-14 | 25 |
| L01-8140 | L1 - Tile Flooring @ Kitchen | 12 | 12 | 07-Jul-14 | 22-Jul-14 | 23 |
| L01-8142 | L1 - Folding Partitions @ Ballrooms | 10 | 10 | 07-Jul-14 | 18-Jul-14 | 25 |
| L01-8128 | L1 - Bath Specialties | 3 | 3 | 18-Jul-14 | 22-Jul-14 | 23 |
| L01-8138 | L1 - Toilet Partitions | 3 | 3 | 18-Jul-14 | 22-Jul-14 | 23 |
| L01-8124 | L1 - Flooring @ Ballrooms | 8 | 8 | 23-Jul-14 | 01-Aug-14 | 14 |
| L01-8126 | L1 - Doors & Hardware | 8 | 8 | 24-Jul-14 | 04-Aug-14 | 14 |
| L01-8130 | L1 - Ballrooms / Kitchen / Restrooms Substantially Cc | 0 | 0 | | 04-Aug-14 | 14 |
| L01-8132 | L1 - Contractor Pre-Punchlist | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 28 |
| L01-8134 | L1 - Pre-Clean | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 23 |
| L01-8114 | L1 - Signage | 3 | 3 | 13-Aug-14 | 15-Aug-14 | 19 |
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8100 | L2 - Insulation | 5 | 5 | 28-Apr-14 | 02-May-14 | 20 |
| L02-6026 | L2 - Pull Wire | 6 | 6 | 28-Apr-14 | 05-May-14 | 68 |
| L02-8102 | L2 - GWB Hang / Tape / Finish - (Including Common / | 20 | 20 | 05-May-14 | 02-Jun-14 | 20 |
| L02-8104 | L2 - Int Painting | 10 | 10 | 29-May-14 | 11-Jun-14 | 20 |
| L02-8106 | L2 - Wallcoverings | 6 | 6 | 02-Jun-14 | 09-Jun-14 | 32 |
| L02-8116 | L2 - Finish Carpentry / Millwork | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 25 |
| L02-8120 | L2 - Ceramic Tile / Counter Tops | 8 | 8 | 09-Jun-14 | 18-Jun-14 | 25 |
| L02-8122 | L2 - Plumbing Trim / Finish | 8 | 8 | 11-Jun-14 | 20-Jun-14 | 27 |
| L02-8108 | L2 - Elec Trim / Finish | 10 | 10 | 12-Jun-14 | 25-Jun-14 | 20 |
| L02-8110 | L2 - HVAC Trim / Finish | 10 | 10 | 12-Jun-14 | 25-Jun-14 | 20 |
| L02-8112 | L2 - Fire Sprinkler Trim / Finish | 8 | 8 | 12-Jun-14 | 23-Jun-14 | 22 |

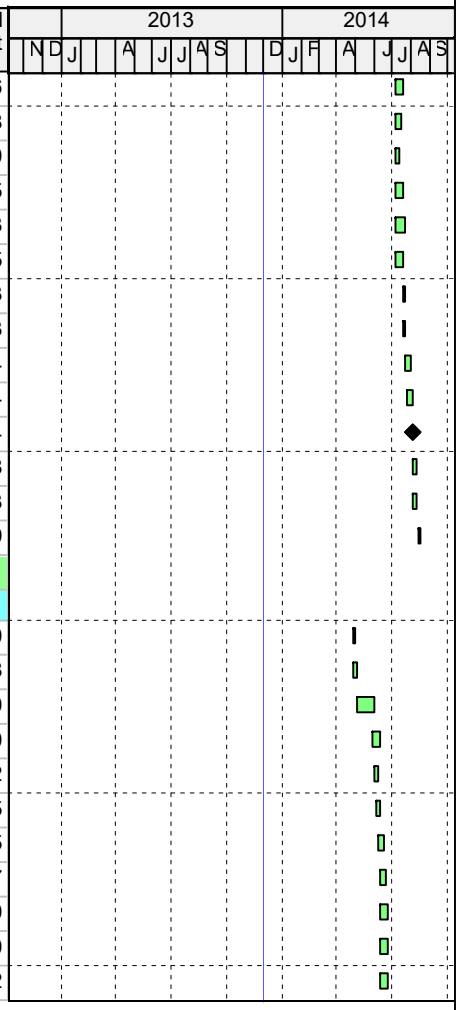



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8118 | L2 - Elec Specialties Trim / Finish | 10 | 10 | 12-Jun-14 | 25-Jun-14 | 20 |
| L02-8136 | L2 - Lockers / Benches @ Locker Rooms | 5 | 5 | 12-Jun-14 | 18-Jun-14 | 31 |
| L02-8128 | L2 - Bath Specialties | 2 | 2 | 23-Jun-14 | 24-Jun-14 | 27 |
| L02-8124 | L2 - Flooring | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 20 |
| L02-8126 | L2 - Doors & Hardware | 5 | 5 | 27-Jun-14 | 03-Jul-14 | 20 |
| L02-8130 | L2 - Admin / Employee Rooms Substantially Complet | 0 | 0 | | 03-Jul-14 | 20 |
| L02-8132 | L2 - Contractor Pre-Punchlist | 5 | 5 | 07-Jul-14 | 11-Jul-14 | 54 |
| L02-8134 | L2 - Pre-Clean | 5 | 5 | 07-Jul-14 | 11-Jul-14 | 49 |
| **Corridors** | | | | | | |
| L02-8200 | L2 - Final Paint @ Common / Public Areas | 5 | 5 | 07-Jul-14 | 11-Jul-14 | 20 |
| L02-8114 | L2 - Signage | 3 | 3 | 14-Jul-14 | 16-Jul-14 | 46 |
| L02-8202 | L2 - Elec Trim / Finish @ Common / Public Areas | 5 | 5 | 14-Jul-14 | 18-Jul-14 | 20 |
| L02-8204 | L2 - Mech Trim / Finish @ Common / Public Areas | 5 | 5 | 14-Jul-14 | 18-Jul-14 | 20 |
| L02-8206 | L2 - Flooring @ Corridors | 5 | 5 | 21-Jul-14 | 25-Jul-14 | 39 |
| L02-8208 | L2 - Final Clean | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 39 |
| L02-8210 | L2 - Owner Walk / Create Punchlist | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 39 |
| L02-8212 | L2 - Final Punchlist | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 39 |
| L02-8214 | L2 - Floor Complete | 0 | 0 | | 11-Aug-14 | 39 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L03-8102S | Stock GWB | 2 | 2 | 05-Mar-14 | 06-Mar-14 | 92 |
| L04-8102S | Stock GWB | 2 | 2 | 06-Mar-14 | 07-Mar-14 | 91 |
| L03-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 07-Mar-14 | 17-Mar-14 | 92 |
| L04-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 10-Mar-14 | 18-Mar-14 | 91 |
| L05-8102S | Stock GWB | 2 | 2 | 13-Mar-14 | 14-Mar-14 | 86 |
| L05-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 17-Mar-14 | 25-Mar-14 | 86 |

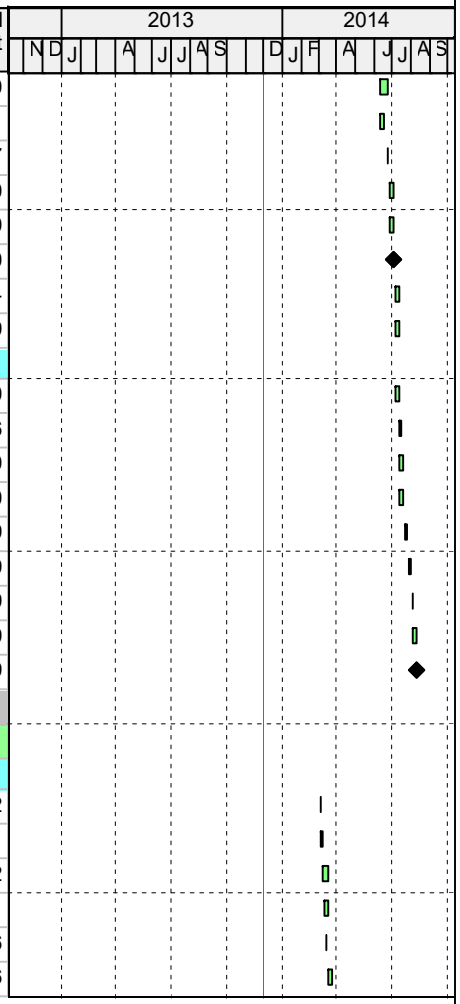



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8102S | Stock GWB | 2 | 2 | 20-Mar-14 | 21-Mar-14 | 81 |
| L06-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 24-Mar-14 | 01-Apr-14 | 81 |
| L03-8104 | Primer Paint Coat | 2 | 2 | 26-Mar-14 | 27-Mar-14 | 92 |
| L04-8104 | Primer Paint Coat | 2 | 2 | 27-Mar-14 | 28-Mar-14 | 91 |
| L07-8102S | Stock GWB | 2 | 2 | 27-Mar-14 | 28-Mar-14 | 76 |
| L03-8120 | Install Casework/Countertops | 5 | 5 | 28-Mar-14 | 03-Apr-14 | 92 |
| L04-8120 | Install Casework/Countertops | 5 | 5 | 31-Mar-14 | 04-Apr-14 | 91 |
| L07-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 31-Mar-14 | 08-Apr-14 | 76 |
| L03-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 02-Apr-14 | 08-Apr-14 | 92 |
| L04-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 03-Apr-14 | 09-Apr-14 | 91 |
| L05-8104 | Primer Paint Coat | 2 | 2 | 03-Apr-14 | 04-Apr-14 | 86 |
| L08-8102S | Stock GWB | 2 | 2 | 03-Apr-14 | 04-Apr-14 | 71 |
| L03-8116 | Install Wood Base | 3 | 3 | 04-Apr-14 | 08-Apr-14 | 92 |
| L03-8128 | Install Tub Glazing | 4 | 4 | 07-Apr-14 | 10-Apr-14 | 92 |
| L04-8116 | Install Wood Base | 3 | 3 | 07-Apr-14 | 09-Apr-14 | 91 |
| L05-8120 | Install Casework/Countertops | 5 | 5 | 07-Apr-14 | 11-Apr-14 | 86 |
| L08-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 07-Apr-14 | 15-Apr-14 | 71 |
| L04-8128 | Install Tub Glazing | 4 | 4 | 08-Apr-14 | 11-Apr-14 | 91 |
| L03-8105 | First Coat Finish Paint | 5 | 5 | 09-Apr-14 | 15-Apr-14 | 92 |
| L04-8105 | First Coat Finish Paint | 5 | 5 | 10-Apr-14 | 16-Apr-14 | 91 |
| L05-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 10-Apr-14 | 16-Apr-14 | 86 |
| L06-8104 | Primer Paint Coat | 2 | 2 | 10-Apr-14 | 11-Apr-14 | 81 |
| L09-8102S | Stock GWB | 2 | 2 | 10-Apr-14 | 11-Apr-14 | 66 |
| L03-8124 | Flooring @ Guest Rooms | 5 | 5 | 11-Apr-14 | 17-Apr-14 | 92 |
| L04-8124 | Flooring @ Guest Rooms | 5 | 5 | 14-Apr-14 | 18-Apr-14 | 91 |
| L05-8116 | Install Wood Base | 3 | 3 | 14-Apr-14 | 16-Apr-14 | 86 |
| L06-8120 | Install Casework/Countertops | 5 | 5 | 14-Apr-14 | 18-Apr-14 | 81 |

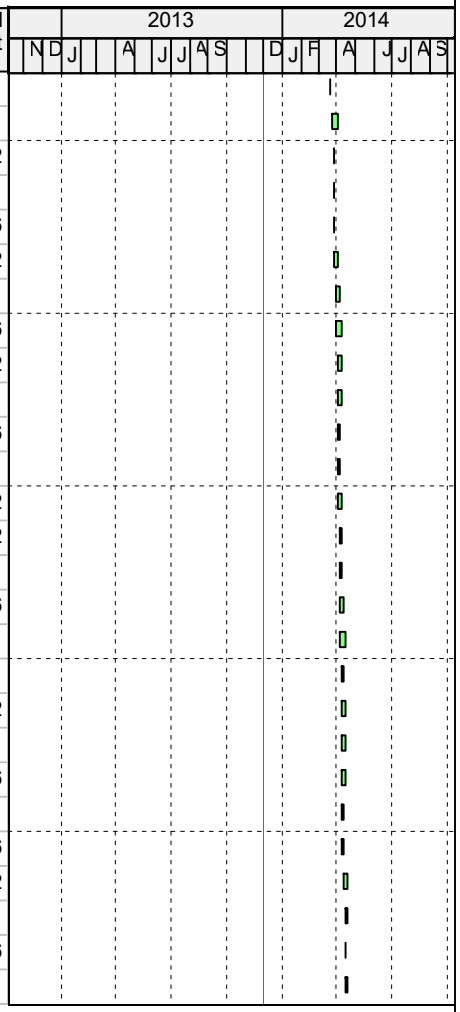



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 14-Apr-14 | 22-Apr-14 | 66 |
| L05-8128 | Install Tub Glazing | 4 | 4 | 15-Apr-14 | 18-Apr-14 | 86 |
| L03-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 16-Apr-14 | 18-Apr-14 | 92 |
| L04-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 17-Apr-14 | 21-Apr-14 | 91 |
| L05-8105 | First Coat Finish Paint | 5 | 5 | 17-Apr-14 | 23-Apr-14 | 86 |
| L06-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 17-Apr-14 | 23-Apr-14 | 81 |
| L07-8104 | Primer Paint Coat | 2 | 2 | 17-Apr-14 | 18-Apr-14 | 76 |
| L10-8102S | Stock GWB | 2 | 2 | 17-Apr-14 | 18-Apr-14 | 61 |
| L03-8107 | Final Coat Finish Paint | 5 | 5 | 21-Apr-14 | 25-Apr-14 | 92 |
| L05-8124 | Flooring @ Guest Rooms | 5 | 5 | 21-Apr-14 | 25-Apr-14 | 86 |
| L06-8116 | Install Wood Base | 3 | 3 | 21-Apr-14 | 23-Apr-14 | 81 |
| L07-8120 | Install Casework/Countertops | 5 | 5 | 21-Apr-14 | 25-Apr-14 | 76 |
| L10-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 21-Apr-14 | 29-Apr-14 | 61 |
| L04-8107 | Final Coat Finish Paint | 5 | 5 | 22-Apr-14 | 28-Apr-14 | 91 |
| L06-8128 | Install Tub Glazing | 4 | 4 | 22-Apr-14 | 25-Apr-14 | 81 |
| L03-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 24-Apr-14 | 30-Apr-14 | 96 |
| L03-8108 | Elec Trim / Finish | 5 | 5 | 24-Apr-14 | 30-Apr-14 | 96 |
| L03-8110 | HVAC Trim / Finish | 5 | 5 | 24-Apr-14 | 30-Apr-14 | 96 |
| L03-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 24-Apr-14 | 30-Apr-14 | 96 |
| L05-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 24-Apr-14 | 28-Apr-14 | 86 |
| L06-8105 | First Coat Finish Paint | 5 | 5 | 24-Apr-14 | 30-Apr-14 | 81 |
| L07-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 24-Apr-14 | 30-Apr-14 | 76 |
| L08-8104 | Primer Paint Coat | 2 | 2 | 24-Apr-14 | 25-Apr-14 | 71 |
| L11-8102S | Stock GWB | 2 | 2 | 24-Apr-14 | 25-Apr-14 | 16 |
| L04-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 25-Apr-14 | 01-May-14 | 95 |
| L04-8108 | Elec Trim / Finish | 5 | 5 | 25-Apr-14 | 01-May-14 | 95 |
| L04-8110 | HVAC Trim / Finish | 5 | 5 | 25-Apr-14 | 01-May-14 | 95 |





© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 25-Apr-14 | 01-May-14 | 95 |
| L03-8126 | Doors & Hardware | 5 | 5 | 28-Apr-14 | 02-May-14 | 92 |
| L03-8118 | Elec Specialties Trim / Finish | 4 | 4 | 28-Apr-14 | 01-May-14 | 95 |
| L06-8124 | Flooring @ Guest Rooms | 5 | 5 | 28-Apr-14 | 02-May-14 | 81 |
| L07-8116 | Install Wood Base | 3 | 3 | 28-Apr-14 | 30-Apr-14 | 76 |
| L08-8120 | Install Casework/Countertops | 5 | 5 | 28-Apr-14 | 02-May-14 | 71 |
| L11-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 28-Apr-14 | 06-May-14 | 16 |
| L04-8126 | Doors & Hardware | 5 | 5 | 29-Apr-14 | 05-May-14 | 91 |
| L04-8118 | Elec Specialties Trim / Finish | 4 | 4 | 29-Apr-14 | 02-May-14 | 94 |
| L05-8107 | Final Coat Finish Paint | 5 | 5 | 29-Apr-14 | 05-May-14 | 86 |
| L07-8128 | Install Tub Glazing | 4 | 4 | 29-Apr-14 | 02-May-14 | 76 |
| L06-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 01-May-14 | 05-May-14 | 81 |
| L07-8105 | First Coat Finish Paint | 5 | 5 | 01-May-14 | 07-May-14 | 76 |
| L08-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 01-May-14 | 07-May-14 | 71 |
| L09-8104 | Primer Paint Coat | 2 | 2 | 01-May-14 | 02-May-14 | 66 |
| L03-8114 | Signage (By Owner) | 3 | 3 | 02-May-14 | 06-May-14 | 92 |
| L05-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 02-May-14 | 08-May-14 | 90 |
| L05-8108 | Elec Trim / Finish | 5 | 5 | 02-May-14 | 08-May-14 | 90 |
| L05-8110 | HVAC Trim / Finish | 5 | 5 | 02-May-14 | 08-May-14 | 90 |
| L05-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 02-May-14 | 08-May-14 | 90 |
| L04-8114 | Signage (By Owner) | 3 | 3 | 05-May-14 | 07-May-14 | 91 |
| L07-8124 | Flooring @ Guest Rooms | 5 | 5 | 05-May-14 | 09-May-14 | 76 |
| L08-8116 | Install Wood Base | 3 | 3 | 05-May-14 | 07-May-14 | 71 |
| L09-8120 | Install Casework/Countertops | 5 | 5 | 05-May-14 | 09-May-14 | 66 |
| L05-8126 | Doors & Hardware | 5 | 5 | 06-May-14 | 12-May-14 | 86 |
| L05-8118 | Elec Specialties Trim / Finish | 4 | 4 | 06-May-14 | 09-May-14 | 89 |
| L06-8107 | Final Coat Finish Paint | 5 | 5 | 06-May-14 | 12-May-14 | 81 |

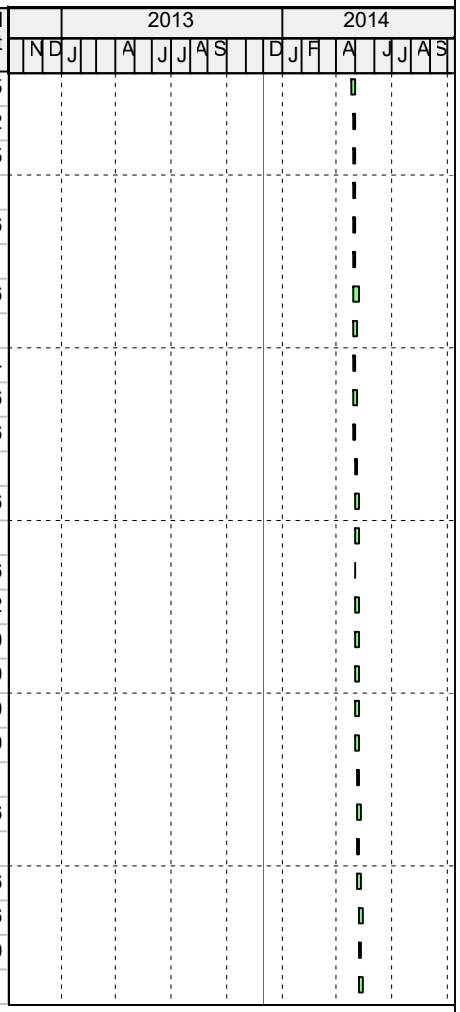



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8128 | Install Tub Glazing | 4 | 4 | 06-May-14 | 09-May-14 | 71 |
| L03-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 06-May-14 | 92 |
| L03-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 07-May-14 | 13-May-14 | 95 |
| L03-8134 | Pre-Clean Guestrooms | 5 | 5 | 07-May-14 | 13-May-14 | 92 |
| L04-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 07-May-14 | 91 |
| L04-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 08-May-14 | 14-May-14 | 94 |
| L04-8134 | Pre-Clean Guestrooms | 5 | 5 | 08-May-14 | 14-May-14 | 91 |
| L07-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 08-May-14 | 12-May-14 | 76 |
| L08-8105 | First Coat Finish Paint | 5 | 5 | 08-May-14 | 14-May-14 | 71 |
| L09-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 08-May-14 | 14-May-14 | 66 |
| L10-8104 | Primer Paint Coat | 2 | 2 | 08-May-14 | 09-May-14 | 61 |
| L12-8102S | Stock GWB | 2 | 2 | 08-May-14 | 09-May-14 | 46 |
| L06-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 09-May-14 | 15-May-14 | 85 |
| L06-8108 | Elec Trim / Finish | 5 | 5 | 09-May-14 | 15-May-14 | 85 |
| L06-8110 | HVAC Trim / Finish | 5 | 5 | 09-May-14 | 15-May-14 | 85 |
| L06-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 09-May-14 | 15-May-14 | 85 |
| L05-8114 | Signage (By Owner) | 3 | 3 | 12-May-14 | 14-May-14 | 86 |
| L08-8124 | Flooring @ Guest Rooms | 5 | 5 | 12-May-14 | 16-May-14 | 71 |
| L09-8116 | Install Wood Base | 3 | 3 | 12-May-14 | 14-May-14 | 66 |
| L10-8120 | Install Casework/Countertops | 5 | 5 | 12-May-14 | 16-May-14 | 61 |
| L12-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 12-May-14 | 20-May-14 | 46 |
| L06-8126 | Doors & Hardware | 5 | 5 | 13-May-14 | 19-May-14 | 81 |
| L06-8118 | Elec Specialties Trim / Finish | 4 | 4 | 13-May-14 | 16-May-14 | 84 |
| L07-8107 | Final Coat Finish Paint | 5 | 5 | 13-May-14 | 19-May-14 | 76 |
| L09-8128 | Install Tub Glazing | 4 | 4 | 13-May-14 | 16-May-14 | 66 |
| L05-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 14-May-14 | 86 |
| L05-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 15-May-14 | 21-May-14 | 89 |

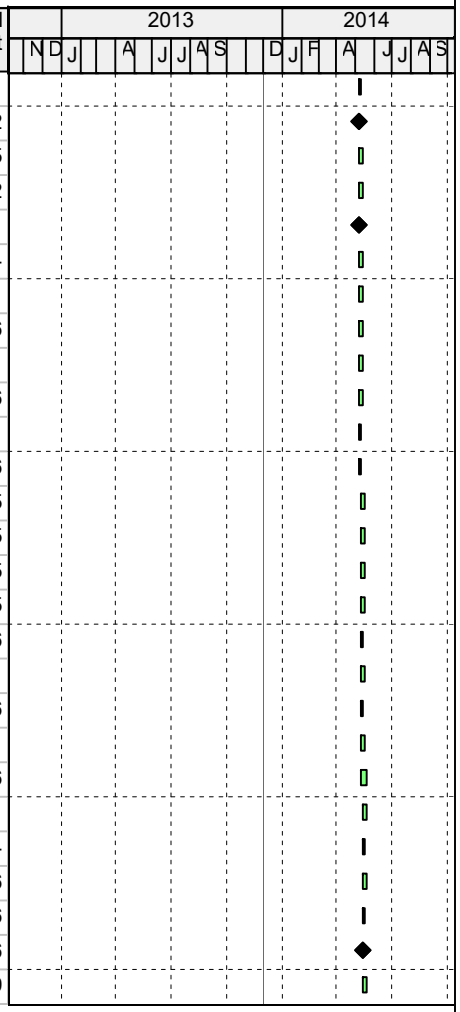



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8134 | Pre-Clean Guestrooms | 5 | 5 | 15-May-14 | 21-May-14 | 86 |
| L08-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 15-May-14 | 19-May-14 | 71 |
| L09-8105 | First Coat Finish Paint | 5 | 5 | 15-May-14 | 21-May-14 | 66 |
| L10-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 15-May-14 | 21-May-14 | 61 |
| L11-8104 | Primer Paint Coat | 2 | 2 | 15-May-14 | 16-May-14 | 16 |
| L14-8102S | Stock GWB | 2 | 2 | 15-May-14 | 16-May-14 | 41 |
| L07-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 16-May-14 | 22-May-14 | 80 |
| L07-8108 | Elec Trim / Finish | 5 | 5 | 16-May-14 | 22-May-14 | 80 |
| L07-8110 | HVAC Trim / Finish | 5 | 5 | 16-May-14 | 22-May-14 | 80 |
| L07-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 16-May-14 | 22-May-14 | 80 |
| L06-8114 | Signage (By Owner) | 3 | 3 | 19-May-14 | 21-May-14 | 81 |
| L09-8124 | Flooring @ Guest Rooms | 5 | 5 | 19-May-14 | 23-May-14 | 66 |
| L10-8116 | Install Wood Base | 3 | 3 | 19-May-14 | 21-May-14 | 61 |
| L11-8120 | Install Casework/Countertops | 5 | 5 | 19-May-14 | 23-May-14 | 16 |
| L14-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 19-May-14 | 28-May-14 | 41 |
| L07-8126 | Doors & Hardware | 5 | 5 | 20-May-14 | 27-May-14 | 76 |
| L07-8118 | Elec Specialties Trim / Finish | 4 | 4 | 20-May-14 | 23-May-14 | 79 |
| L08-8107 | Final Coat Finish Paint | 5 | 5 | 20-May-14 | 27-May-14 | 71 |
| L10-8128 | Install Tub Glazing | 4 | 4 | 20-May-14 | 23-May-14 | 61 |
| L06-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 21-May-14 | 81 |
| L06-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 22-May-14 | 29-May-14 | 84 |
| L06-8134 | Pre-Clean Guestrooms | 5 | 5 | 22-May-14 | 29-May-14 | 81 |
| L09-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 22-May-14 | 27-May-14 | 66 |
| L10-8105 | First Coat Finish Paint | 5 | 5 | 22-May-14 | 29-May-14 | 61 |
| L11-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 22-May-14 | 29-May-14 | 16 |
| L15-8102S | Stock GWB | 2 | 2 | 22-May-14 | 23-May-14 | 36 |
| L08-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 23-May-14 | 30-May-14 | 75 |

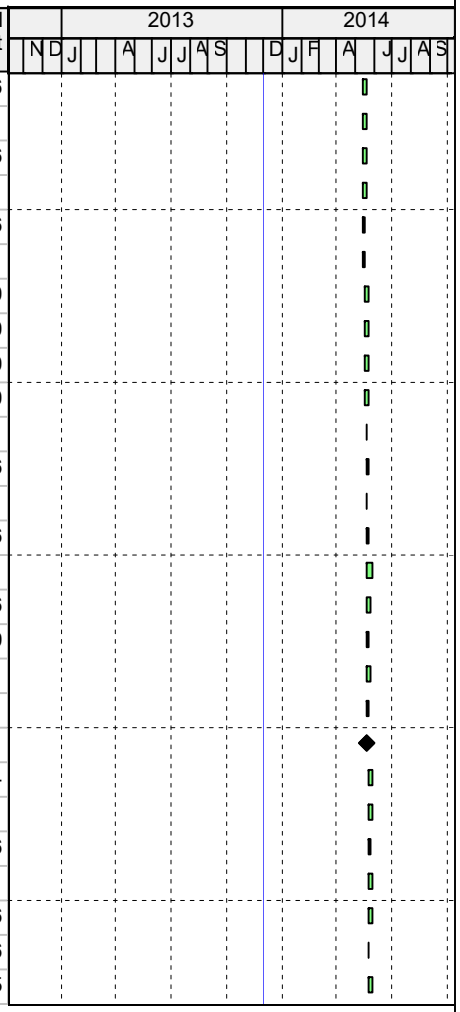


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8108 | Elec Trim / Finish | 5 | 5 | 23-May-14 | 30-May-14 | 75 |
| L08-8110 | HVAC Trim / Finish | 5 | 5 | 23-May-14 | 30-May-14 | 75 |
| L08-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 23-May-14 | 30-May-14 | 75 |
| L07-8114 | Signage (By Owner) | 3 | 3 | 27-May-14 | 29-May-14 | 76 |
| L10-8124 | Flooring @ Guest Rooms | 5 | 5 | 27-May-14 | 02-Jun-14 | 61 |
| L11-8116 | Install Wood Base | 3 | 3 | 27-May-14 | 29-May-14 | 16 |
| L15-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 27-May-14 | 04-Jun-14 | 36 |
| L08-8126 | Doors & Hardware | 5 | 5 | 28-May-14 | 03-Jun-14 | 71 |
| L08-8118 | Elec Specialties Trim / Finish | 4 | 4 | 28-May-14 | 02-Jun-14 | 74 |
| L09-8107 | Final Coat Finish Paint | 5 | 5 | 28-May-14 | 03-Jun-14 | 66 |
| L11-8128 | Install Tub Glazing | 4 | 4 | 28-May-14 | 02-Jun-14 | 16 |
| L07-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 |  | 29-May-14 | 76 |
| L07-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 30-May-14 | 05-Jun-14 | 79 |
| L07-8134 | Pre-Clean Guestrooms | 5 | 5 | 30-May-14 | 05-Jun-14 | 76 |
| L10-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 30-May-14 | 03-Jun-14 | 61 |
| L11-8105 | First Coat Finish Paint | 5 | 5 | 30-May-14 | 05-Jun-14 | 16 |
| L12-8104 | Primer Paint Coat | 2 | 2 | 30-May-14 | 02-Jun-14 | 46 |
| L16-8102S | Stock GWB | 2 | 2 | 30-May-14 | 02-Jun-14 | 31 |
| L09-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 70 |
| L09-8108 | Elec Trim / Finish | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 70 |
| L09-8110 | HVAC Trim / Finish | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 70 |
| L09-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 70 |
| L08-8114 | Signage (By Owner) | 3 | 3 | 03-Jun-14 | 05-Jun-14 | 71 |
| L11-8124 | Flooring @ Guest Rooms | 5 | 5 | 03-Jun-14 | 09-Jun-14 | 16 |
| L12-8120 | Install Casework/Countertops | 5 | 5 | 03-Jun-14 | 09-Jun-14 | 46 |
| L16-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 03-Jun-14 | 11-Jun-14 | 31 |
| L09-8126 | Doors & Hardware | 5 | 5 | 04-Jun-14 | 10-Jun-14 | 66 |





© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8118 | Elec Specialties Trim / Finish | 4 | 4 | 04-Jun-14 | 09-Jun-14 | 69 |
| L10-8107 | Final Coat Finish Paint | 5 | 5 | 04-Jun-14 | 10-Jun-14 | 61 |
| L08-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 05-Jun-14 | 71 |
| L08-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 06-Jun-14 | 12-Jun-14 | 74 |
| L08-8134 | Pre-Clean Guestrooms | 5 | 5 | 06-Jun-14 | 12-Jun-14 | 71 |
| L11-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 06-Jun-14 | 10-Jun-14 | 16 |
| L12-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 06-Jun-14 | 12-Jun-14 | 46 |
| L14-8104 | Primer Paint Coat | 2 | 2 | 06-Jun-14 | 09-Jun-14 | 41 |
| L17-8102S | Stock GWB | 2 | 2 | 06-Jun-14 | 09-Jun-14 | 26 |
| L10-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 09-Jun-14 | 13-Jun-14 | 65 |
| L10-8108 | Elec Trim / Finish | 5 | 5 | 09-Jun-14 | 13-Jun-14 | 65 |
| L10-8110 | HVAC Trim / Finish | 5 | 5 | 09-Jun-14 | 13-Jun-14 | 65 |
| L10-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 09-Jun-14 | 13-Jun-14 | 65 |
| L09-8114 | Signage (By Owner) | 3 | 3 | 10-Jun-14 | 12-Jun-14 | 66 |
| L12-8116 | Install Wood Base | 3 | 3 | 10-Jun-14 | 12-Jun-14 | 46 |
| L14-8120 | Install Casework/Countertops | 5 | 5 | 10-Jun-14 | 16-Jun-14 | 41 |
| L17-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 10-Jun-14 | 18-Jun-14 | 26 |
| L10-8126 | Doors & Hardware | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 61 |
| L10-8118 | Elec Specialties Trim / Finish | 4 | 4 | 11-Jun-14 | 16-Jun-14 | 64 |
| L11-8107 | Final Coat Finish Paint | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 16 |
| L12-8128 | Install Tub Glazing | 4 | 4 | 11-Jun-14 | 16-Jun-14 | 46 |
| L09-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 12-Jun-14 | 66 |
| L09-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 13-Jun-14 | 19-Jun-14 | 69 |
| L09-8134 | Pre-Clean Guestrooms | 5 | 5 | 13-Jun-14 | 19-Jun-14 | 66 |
| L12-8105 | First Coat Finish Paint | 5 | 5 | 13-Jun-14 | 19-Jun-14 | 46 |
| L14-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 13-Jun-14 | 19-Jun-14 | 41 |
| L15-8104 | Primer Paint Coat | 2 | 2 | 13-Jun-14 | 16-Jun-14 | 36 |

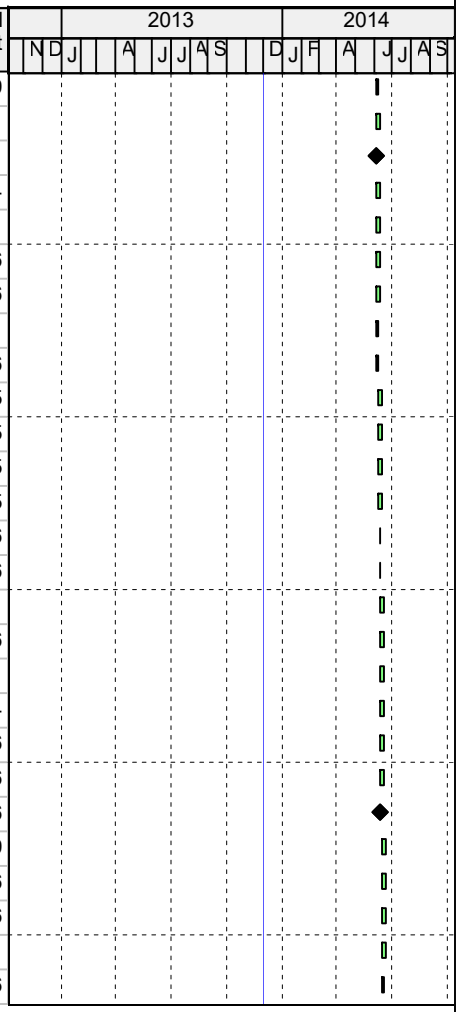



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 16-Jun-14 | 20-Jun-14 | 20 |
| L11-8108 | Elec Trim / Finish | 5 | 5 | 16-Jun-14 | 20-Jun-14 | 20 |
| L11-8110 | HVAC Trim / Finish | 5 | 5 | 16-Jun-14 | 20-Jun-14 | 20 |
| L11-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 16-Jun-14 | 20-Jun-14 | 20 |
| L10-8114 | Signage (By Owner) | 3 | 3 | 17-Jun-14 | 19-Jun-14 | 61 |
| L12-8124 | Flooring @ Guest Rooms | 5 | 5 | 17-Jun-14 | 23-Jun-14 | 46 |
| L14-8116 | Install Wood Base | 3 | 3 | 17-Jun-14 | 19-Jun-14 | 41 |
| L15-8120 | Install Casework/Countertops | 5 | 5 | 17-Jun-14 | 23-Jun-14 | 36 |
| L11-8126 | Doors & Hardware | 5 | 5 | 18-Jun-14 | 24-Jun-14 | 16 |
| L11-8118 | Elec Specialties Trim / Finish | 4 | 4 | 18-Jun-14 | 23-Jun-14 | 19 |
| L14-8128 | Install Tub Glazing | 4 | 4 | 18-Jun-14 | 23-Jun-14 | 41 |
| L10-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 19-Jun-14 | 61 |
| L10-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 20-Jun-14 | 26-Jun-14 | 64 |
| L10-8134 | Pre-Clean Guestrooms | 5 | 5 | 20-Jun-14 | 26-Jun-14 | 61 |
| L12-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 20-Jun-14 | 24-Jun-14 | 46 |
| L14-8105 | First Coat Finish Paint | 5 | 5 | 20-Jun-14 | 26-Jun-14 | 41 |
| L15-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 20-Jun-14 | 26-Jun-14 | 36 |
| L16-8104 | Primer Paint Coat | 2 | 2 | 20-Jun-14 | 23-Jun-14 | 31 |
| L11-8114 | Signage (By Owner) | 3 | 3 | 24-Jun-14 | 26-Jun-14 | 16 |
| L14-8124 | Flooring @ Guest Rooms | 5 | 5 | 24-Jun-14 | 30-Jun-14 | 41 |
| L15-8116 | Install Wood Base | 3 | 3 | 24-Jun-14 | 26-Jun-14 | 36 |
| L16-8120 | Install Casework/Countertops | 5 | 5 | 24-Jun-14 | 30-Jun-14 | 31 |
| L12-8107 | Final Coat Finish Paint | 5 | 5 | 25-Jun-14 | 01-Jul-14 | 46 |
| L15-8128 | Install Tub Glazing | 4 | 4 | 25-Jun-14 | 30-Jun-14 | 36 |
| L11-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 26-Jun-14 | 16 |
| L11-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 27-Jun-14 | 03-Jul-14 | 19 |
| L11-8134 | Pre-Clean Guestrooms | 5 | 5 | 27-Jun-14 | 03-Jul-14 | 16 |

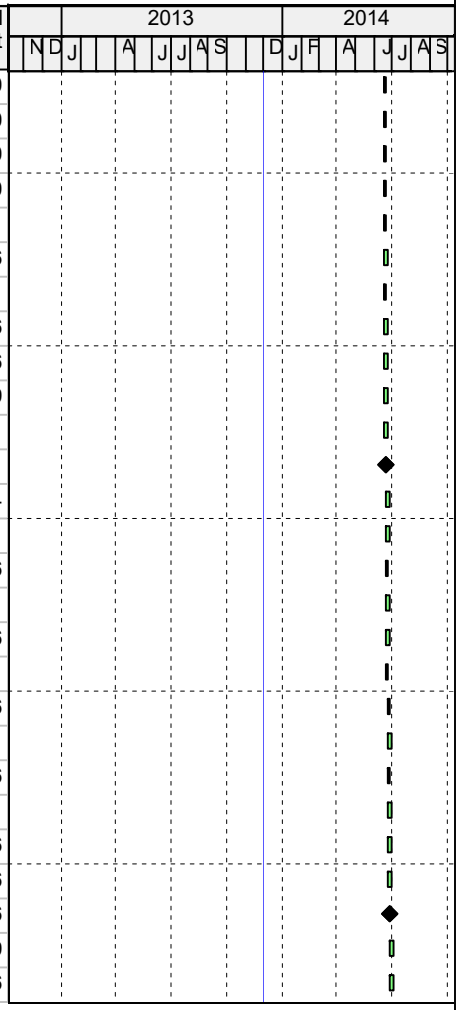


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 27-Jun-14 | 01-Jul-14 | 41 |
| L15-8105 | First Coat Finish Paint | 5 | 5 | 27-Jun-14 | 03-Jul-14 | 36 |
| L16-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 27-Jun-14 | 03-Jul-14 | 31 |
| L17-8104 | Primer Paint Coat | 2 | 2 | 27-Jun-14 | 30-Jun-14 | 26 |
| L12-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 30-Jun-14 | 07-Jul-14 | 50 |
| L12-8108 | Elec Trim / Finish | 5 | 5 | 30-Jun-14 | 07-Jul-14 | 50 |
| L12-8110 | HVAC Trim / Finish | 5 | 5 | 30-Jun-14 | 07-Jul-14 | 50 |
| L12-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 30-Jun-14 | 07-Jul-14 | 50 |
| L15-8124 | Flooring @ Guest Rooms | 5 | 5 | 01-Jul-14 | 08-Jul-14 | 36 |
| L16-8116 | Install Wood Base | 3 | 3 | 01-Jul-14 | 03-Jul-14 | 31 |
| L17-8120 | Install Casework/Countertops | 5 | 5 | 01-Jul-14 | 08-Jul-14 | 26 |
| L12-8126 | Doors & Hardware | 5 | 5 | 02-Jul-14 | 09-Jul-14 | 46 |
| L12-8118 | Elec Specialties Trim / Finish | 4 | 4 | 02-Jul-14 | 08-Jul-14 | 49 |
| L14-8107 | Final Coat Finish Paint | 5 | 5 | 02-Jul-14 | 09-Jul-14 | 41 |
| L16-8128 | Install Tub Glazing | 4 | 4 | 02-Jul-14 | 08-Jul-14 | 31 |
| L15-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 07-Jul-14 | 09-Jul-14 | 36 |
| L16-8105 | First Coat Finish Paint | 5 | 5 | 07-Jul-14 | 11-Jul-14 | 31 |
| L17-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 07-Jul-14 | 11-Jul-14 | 26 |
| L14-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 08-Jul-14 | 14-Jul-14 | 45 |
| L14-8108 | Elec Trim / Finish | 5 | 5 | 08-Jul-14 | 14-Jul-14 | 45 |
| L14-8110 | HVAC Trim / Finish | 5 | 5 | 08-Jul-14 | 14-Jul-14 | 45 |
| L14-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 08-Jul-14 | 14-Jul-14 | 45 |
| L12-8114 | Signage (By Owner) | 3 | 3 | 09-Jul-14 | 11-Jul-14 | 46 |
| L16-8124 | Flooring @ Guest Rooms | 5 | 5 | 09-Jul-14 | 15-Jul-14 | 31 |
| L17-8116 | Install Wood Base | 3 | 3 | 09-Jul-14 | 11-Jul-14 | 26 |
| L14-8126 | Doors & Hardware | 5 | 5 | 10-Jul-14 | 16-Jul-14 | 41 |
| L14-8118 | Elec Specialties Trim / Finish | 4 | 4 | 10-Jul-14 | 15-Jul-14 | 44 |





© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8107 | Final Coat Finish Paint | 5 | 5 | 10-Jul-14 | 16-Jul-14 | 36 |
| L17-8128 | Install Tub Glazing | 4 | 4 | 10-Jul-14 | 15-Jul-14 | 26 |
| L12-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 11-Jul-14 | 46 |
| L12-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 14-Jul-14 | 18-Jul-14 | 49 |
| L12-8134 | Pre-Clean Guestrooms | 5 | 5 | 14-Jul-14 | 18-Jul-14 | 46 |
| L16-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 14-Jul-14 | 16-Jul-14 | 31 |
| L17-8105 | First Coat Finish Paint | 5 | 5 | 14-Jul-14 | 18-Jul-14 | 26 |
| L15-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 40 |
| L15-8108 | Elec Trim / Finish | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 40 |
| L15-8110 | HVAC Trim / Finish | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 40 |
| L15-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 40 |
| L14-8114 | Signage (By Owner) | 3 | 3 | 16-Jul-14 | 18-Jul-14 | 41 |
| L17-8124 | Flooring @ Guest Rooms | 5 | 5 | 16-Jul-14 | 22-Jul-14 | 26 |
| L15-8126 | Doors & Hardware | 5 | 5 | 17-Jul-14 | 23-Jul-14 | 36 |
| L15-8118 | Elec Specialties Trim / Finish | 4 | 4 | 17-Jul-14 | 22-Jul-14 | 39 |
| L16-8107 | Final Coat Finish Paint | 5 | 5 | 17-Jul-14 | 23-Jul-14 | 31 |
| L14-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 18-Jul-14 | 41 |
| L14-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 21-Jul-14 | 25-Jul-14 | 44 |
| L14-8134 | Pre-Clean Guestrooms | 5 | 5 | 21-Jul-14 | 25-Jul-14 | 41 |
| L17-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 21-Jul-14 | 23-Jul-14 | 26 |
| L16-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 22-Jul-14 | 28-Jul-14 | 35 |
| L16-8108 | Elec Trim / Finish | 5 | 5 | 22-Jul-14 | 28-Jul-14 | 35 |
| L16-8110 | HVAC Trim / Finish | 5 | 5 | 22-Jul-14 | 28-Jul-14 | 35 |
| L16-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 22-Jul-14 | 28-Jul-14 | 35 |
| L15-8114 | Signage (By Owner) | 3 | 3 | 23-Jul-14 | 25-Jul-14 | 36 |
| L16-8126 | Doors & Hardware | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 31 |
| L16-8118 | Elec Specialties Trim / Finish | 4 | 4 | 24-Jul-14 | 29-Jul-14 | 34 |

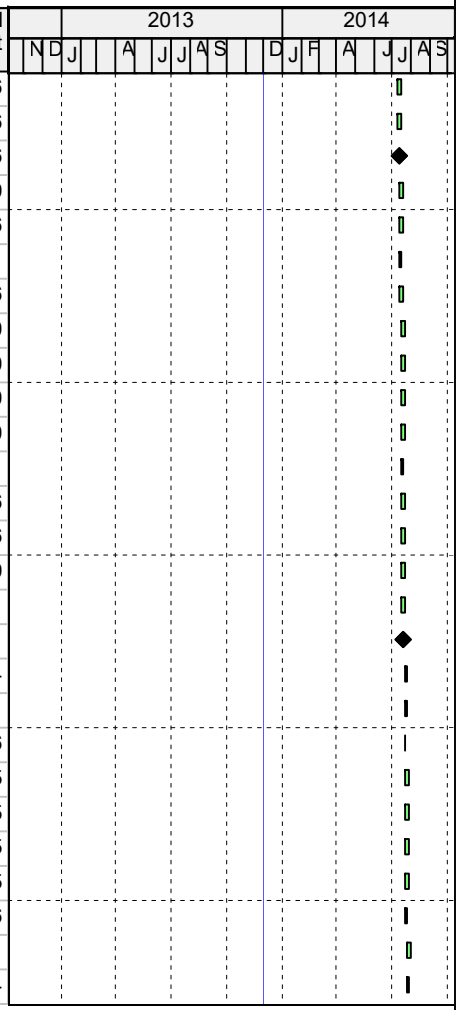



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8107 | Final Coat Finish Paint | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 26 |
| L15-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 25-Jul-14 | 36 |
| L15-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 39 |
| L15-8134 | Pre-Clean Guestrooms | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 36 |
| L17-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 29-Jul-14 | 04-Aug-14 | 30 |
| L17-8108 | Elec Trim / Finish | 5 | 5 | 29-Jul-14 | 04-Aug-14 | 30 |
| L17-8110 | HVAC Trim / Finish | 5 | 5 | 29-Jul-14 | 04-Aug-14 | 30 |
| L17-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 29-Jul-14 | 04-Aug-14 | 30 |
| L16-8114 | Signage (By Owner) | 3 | 3 | 30-Jul-14 | 01-Aug-14 | 31 |
| L17-8126 | Doors & Hardware | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 26 |
| L17-8118 | Elec Specialties Trim / Finish | 4 | 4 | 31-Jul-14 | 05-Aug-14 | 29 |
| L16-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 01-Aug-14 | 31 |
| L16-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 34 |
| L16-8134 | Pre-Clean Guestrooms | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 31 |
| L17-8114 | Signage (By Owner) | 3 | 3 | 06-Aug-14 | 08-Aug-14 | 26 |
| L17-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 08-Aug-14 | 26 |
| L17-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 29 |
| L17-8134 | Pre-Clean Guestrooms | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 26 |
| **Pool Area** | | | | | | |
| L03-8216 | L3 - Pool Surfaces / Finishes | 16 | 16 | 08-Sep-14 | 29-Sep-14 | 0 |
| L03-8218 | L3 - Pool Equipment | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 0 |
| **Corridors / Common / Public Areas** | | | | | | |
| L03-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 21-Apr-14 | 25-Apr-14 | 96 |
| L03-8206 | Flooring @ Corridors | 2 | 2 | 21-Apr-14 | 22-Apr-14 | 92 |
| L04-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 22-Apr-14 | 28-Apr-14 | 95 |
| L04-8206 | Flooring @ Corridors | 2 | 2 | 22-Apr-14 | 23-Apr-14 | 91 |
| L03-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 28-Apr-14 | 29-Apr-14 | 97 |

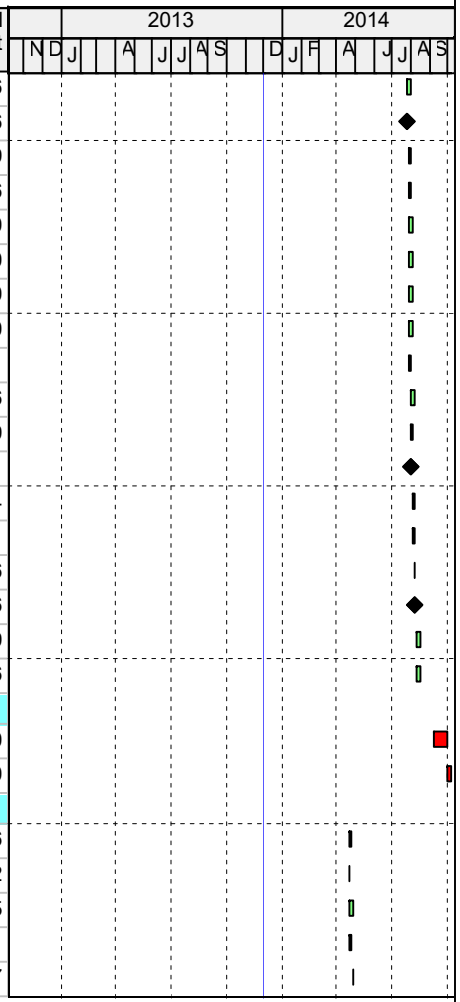


Actual Work | Remaining Work | Critical Remai... | Milestone | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 28-Apr-14 | 29-Apr-14 | 97 |
| L04-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 29-Apr-14 | 30-Apr-14 | 96 |
| L04-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 29-Apr-14 | 30-Apr-14 | 96 |
| L05-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 29-Apr-14 | 05-May-14 | 90 |
| L05-8206 | Flooring @ Corridors | 2 | 2 | 29-Apr-14 | 30-Apr-14 | 86 |
| L05-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 06-May-14 | 07-May-14 | 91 |
| L05-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 06-May-14 | 07-May-14 | 91 |
| L06-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 06-May-14 | 12-May-14 | 85 |
| L06-8206 | Flooring @ Corridors | 2 | 2 | 06-May-14 | 07-May-14 | 81 |
| L06-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 13-May-14 | 14-May-14 | 86 |
| L06-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 13-May-14 | 14-May-14 | 86 |
| L07-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 13-May-14 | 19-May-14 | 80 |
| L07-8206 | Flooring @ Corridors | 2 | 2 | 13-May-14 | 14-May-14 | 76 |
| L03-8208 | Final Clean | 3 | 3 | 14-May-14 | 16-May-14 | 92 |
| L04-8208 | Final Clean | 3 | 3 | 15-May-14 | 19-May-14 | 91 |
| L03-8210 | Owner Walk / Create Punchlist | 1 | 1 | 19-May-14 | 19-May-14 | 92 |
| L03-8212 | Resolve Final Punchlist | 5 | 5 | 20-May-14 | 27-May-14 | 92 |
| L04-8210 | Owner Walk / Create Punchlist | 1 | 1 | 20-May-14 | 20-May-14 | 91 |
| L07-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 20-May-14 | 21-May-14 | 81 |
| L07-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 20-May-14 | 21-May-14 | 81 |
| L08-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 20-May-14 | 27-May-14 | 75 |
| L08-8206 | Flooring @ Corridors | 2 | 2 | 20-May-14 | 21-May-14 | 71 |
| L04-8212 | Resolve Final Punchlist | 5 | 5 | 21-May-14 | 28-May-14 | 91 |
| L05-8208 | Final Clean | 3 | 3 | 22-May-14 | 27-May-14 | 86 |
| L03-8214 | Floor Complete | 0 | 0 | | 27-May-14 | 92 |
| L05-8210 | Owner Walk / Create Punchlist | 1 | 1 | 28-May-14 | 28-May-14 | 86 |
| L08-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 28-May-14 | 29-May-14 | 76 |

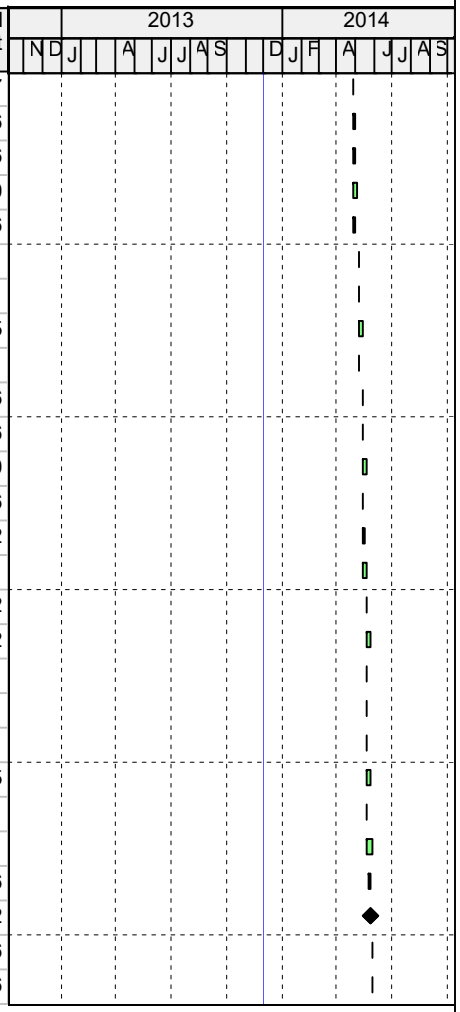



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 28-May-14 | 29-May-14 | 76 |
| L09-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 28-May-14 | 03-Jun-14 | 70 |
| L09-8206 | Flooring @ Corridors | 2 | 2 | 28-May-14 | 29-May-14 | 66 |
| L04-8214 | Floor Complete | 0 | 0 | | 28-May-14 | 91 |
| L05-8212 | Resolve Final Punchlist | 5 | 5 | 29-May-14 | 04-Jun-14 | 86 |
| L06-8208 | Final Clean | 3 | 3 | 30-May-14 | 03-Jun-14 | 81 |
| L06-8210 | Owner Walk / Create Punchlist | 1 | 1 | 04-Jun-14 | 04-Jun-14 | 81 |
| L09-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 04-Jun-14 | 05-Jun-14 | 71 |
| L09-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 04-Jun-14 | 05-Jun-14 | 71 |
| L10-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 04-Jun-14 | 10-Jun-14 | 65 |
| L10-8206 | Flooring @ Corridors | 2 | 2 | 04-Jun-14 | 05-Jun-14 | 61 |
| L05-8214 | Floor Complete | 0 | 0 | | 04-Jun-14 | 86 |
| L06-8212 | Resolve Final Punchlist | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 81 |
| L07-8208 | Final Clean | 3 | 3 | 06-Jun-14 | 10-Jun-14 | 76 |
| L07-8210 | Owner Walk / Create Punchlist | 1 | 1 | 11-Jun-14 | 11-Jun-14 | 76 |
| L10-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 11-Jun-14 | 12-Jun-14 | 66 |
| L10-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 11-Jun-14 | 12-Jun-14 | 66 |
| L11-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 20 |
| L11-8206 | Flooring @ Corridors | 2 | 2 | 11-Jun-14 | 12-Jun-14 | 16 |
| L06-8214 | Floor Complete | 0 | 0 | | 11-Jun-14 | 81 |
| L07-8212 | Resolve Final Punchlist | 5 | 5 | 12-Jun-14 | 18-Jun-14 | 76 |
| L08-8208 | Final Clean | 3 | 3 | 13-Jun-14 | 17-Jun-14 | 71 |
| L08-8210 | Owner Walk / Create Punchlist | 1 | 1 | 18-Jun-14 | 18-Jun-14 | 71 |
| L11-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 18-Jun-14 | 19-Jun-14 | 21 |
| L11-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 18-Jun-14 | 19-Jun-14 | 21 |
| L07-8214 | Floor Complete | 0 | 0 | | 18-Jun-14 | 76 |
| L08-8212 | Resolve Final Punchlist | 5 | 5 | 19-Jun-14 | 25-Jun-14 | 71 |

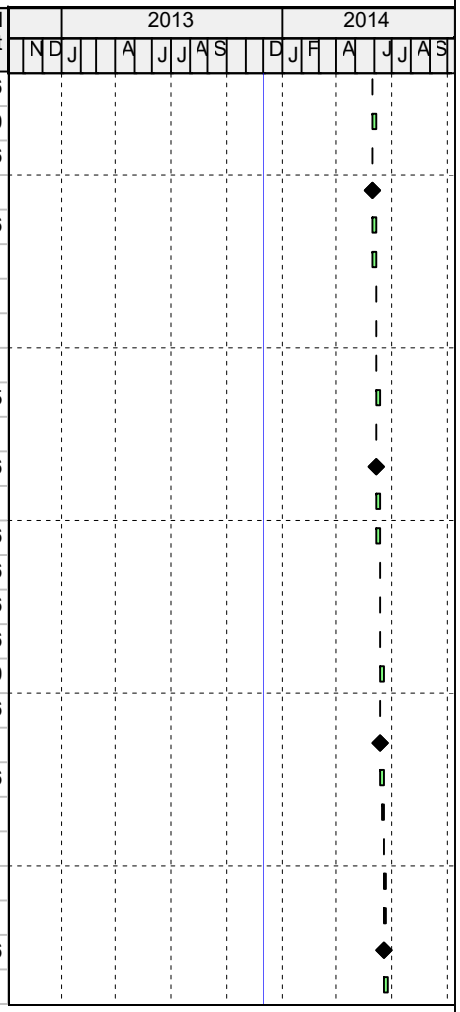



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8208 | Final Clean | 3 | 3 | 20-Jun-14 | 24-Jun-14 | 66 |
| L09-8210 | Owner Walk / Create Punchlist | 1 | 1 | 25-Jun-14 | 25-Jun-14 | 66 |
| L12-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 25-Jun-14 | 01-Jul-14 | 50 |
| L12-8206 | Flooring @ Corridors | 2 | 2 | 25-Jun-14 | 26-Jun-14 | 46 |
| L08-8214 | Floor Complete | 0 | 0 | | 25-Jun-14 | 71 |
| L09-8212 | Resolve Final Punchlist | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 66 |
| L10-8208 | Final Clean | 3 | 3 | 27-Jun-14 | 01-Jul-14 | 61 |
| L10-8210 | Owner Walk / Create Punchlist | 1 | 1 | 02-Jul-14 | 02-Jul-14 | 61 |
| L12-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 02-Jul-14 | 03-Jul-14 | 51 |
| L12-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 02-Jul-14 | 03-Jul-14 | 51 |
| L14-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 02-Jul-14 | 09-Jul-14 | 45 |
| L14-8206 | Flooring @ Corridors | 2 | 2 | 02-Jul-14 | 03-Jul-14 | 41 |
| L09-8214 | Floor Complete | 0 | 0 | | 02-Jul-14 | 66 |
| L10-8212 | Resolve Final Punchlist | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 61 |
| L11-8208 | Final Clean | 3 | 3 | 07-Jul-14 | 09-Jul-14 | 16 |
| L11-8210 | Owner Walk / Create Punchlist | 1 | 1 | 10-Jul-14 | 10-Jul-14 | 16 |
| L14-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 10-Jul-14 | 11-Jul-14 | 46 |
| L14-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 10-Jul-14 | 11-Jul-14 | 46 |
| L15-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 10-Jul-14 | 16-Jul-14 | 40 |
| L15-8206 | Flooring @ Corridors | 2 | 2 | 10-Jul-14 | 11-Jul-14 | 36 |
| L10-8214 | Floor Complete | 0 | 0 | | 10-Jul-14 | 61 |
| L11-8212 | Resolve Final Punchlist | 5 | 5 | 11-Jul-14 | 17-Jul-14 | 16 |
| L15-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 41 |
| L15-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 41 |
| L16-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 17-Jul-14 | 23-Jul-14 | 35 |
| L16-8206 | Flooring @ Corridors | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 31 |
| L11-8214 | Floor Complete | 0 | 0 | | 17-Jul-14 | 16 |

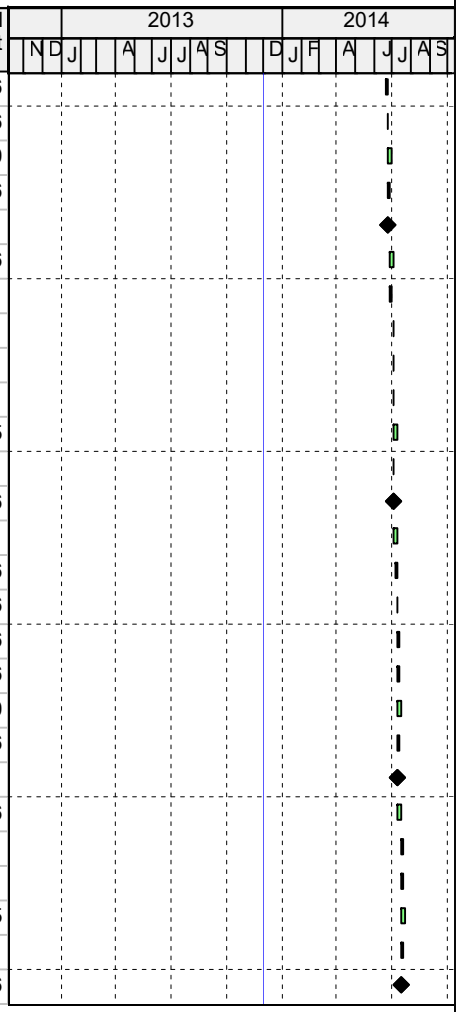



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8208 | Final Clean | 3 | 3 | 21-Jul-14 | 23-Jul-14 | 46 |
| L12-8210 | Owner Walk / Create Punchlist | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 46 |
| L16-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 24-Jul-14 | 25-Jul-14 | 36 |
| L16-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 24-Jul-14 | 25-Jul-14 | 36 |
| L17-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 30 |
| L17-8206 | Flooring @ Corridors | 2 | 2 | 24-Jul-14 | 25-Jul-14 | 26 |
| L12-8212 | Resolve Final Punchlist | 5 | 5 | 25-Jul-14 | 31-Jul-14 | 46 |
| L14-8208 | Final Clean | 3 | 3 | 28-Jul-14 | 30-Jul-14 | 41 |
| L14-8210 | Owner Walk / Create Punchlist | 1 | 1 | 31-Jul-14 | 31-Jul-14 | 41 |
| L17-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 31-Jul-14 | 01-Aug-14 | 31 |
| L17-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 31-Jul-14 | 01-Aug-14 | 31 |
| L12-8214 | Floor Complete | 0 | 0 | | 31-Jul-14 | 46 |
| L14-8212 | Resolve Final Punchlist | 5 | 5 | 01-Aug-14 | 07-Aug-14 | 41 |
| L15-8208 | Final Clean | 3 | 3 | 04-Aug-14 | 06-Aug-14 | 36 |
| L15-8210 | Owner Walk / Create Punchlist | 1 | 1 | 07-Aug-14 | 07-Aug-14 | 36 |
| L14-8214 | Floor Complete | 0 | 0 | | 07-Aug-14 | 41 |
| L15-8212 | Resolve Final Punchlist | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 36 |
| L16-8208 | Final Clean | 3 | 3 | 11-Aug-14 | 13-Aug-14 | 31 |
| L16-8210 | Owner Walk / Create Punchlist | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 31 |
| L15-8214 | Floor Complete | 0 | 0 | | 14-Aug-14 | 36 |
| L16-8212 | Resolve Final Punchlist | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 31 |
| L17-8208 | Final Clean | 3 | 3 | 18-Aug-14 | 20-Aug-14 | 26 |
| L17-8210 | Owner Walk / Create Punchlist | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 26 |
| L16-8214 | Floor Complete | 0 | 0 | | 21-Aug-14 | 31 |
| L17-8212 | Resolve Final Punchlist | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 26 |
| L17-8214 | Floor Complete | 0 | 0 | | 28-Aug-14 | 26 |
| **Mech Penthouse** | | | | | | |

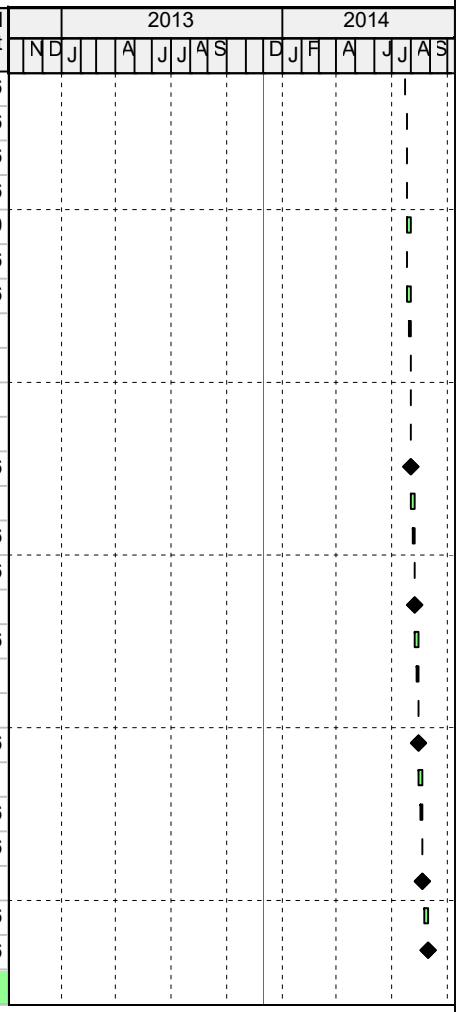



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-8100 | PH - Insulation | 3 | 3 | 16-Jun-14 | 18-Jun-14 | 38 |
| PH-6026 | PH - Pull Wire | 5 | 5 | 16-Jun-14 | 20-Jun-14 | 57 |
| PH-8102 | PH - GWB Hang / Tape / Finish - (Including Common | 10 | 10 | 19-Jun-14 | 02-Jul-14 | 38 |
| PH-8104 | PH - Int Painting | 4 | 4 | 30-Jun-14 | 03-Jul-14 | 38 |
| PH-8108 | PH - Elec Trim / Finish | 10 | 10 | 07-Jul-14 | 18-Jul-14 | 38 |
| PH-8110 | PH - HVAC Trim / Finish | 10 | 10 | 07-Jul-14 | 18-Jul-14 | 38 |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 5 | 5 | 07-Jul-14 | 11-Jul-14 | 43 |
| PH-8114 | PH - Signage | 2 | 2 | 07-Jul-14 | 08-Jul-14 | 54 |
| PH-8118 | PH - Elec Specialties Trim / Finish | 4 | 4 | 07-Jul-14 | 10-Jul-14 | 44 |
| PH-8116 | PH - Finish Carpentry / Millwork | 5 | 5 | 08-Jul-14 | 14-Jul-14 | 42 |
| PH-8122 | PH - Plumbing Trim / Finish | 5 | 5 | 14-Jul-14 | 18-Jul-14 | 43 |
| PH-8124 | PH - Flooring | 4 | 4 | 21-Jul-14 | 24-Jul-14 | 38 |
| PH-8126 | PH - Doors & Hardware | 3 | 3 | 23-Jul-14 | 25-Jul-14 | 38 |
| PH-8130 | PH - Guest Rooms Substantially Complete | 0 | 0 | | 25-Jul-14 | 38 |
| PH-8132 | PH - Contractor Pre-Punchlist | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 39 |
| PH-8134 | PH - Pre-Clean | 3 | 3 | 28-Jul-14 | 30-Jul-14 | 38 |
| PH-8208 | PH - Final Clean | 3 | 3 | 31-Jul-14 | 04-Aug-14 | 38 |
| PH-8210 | PH - Owner Walk / Create Punchlist | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 38 |
| PH-8212 | PH - Final Punchlist | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 38 |
| PH-8214 | PH - Floor Complete | 0 | 0 | | 12-Aug-14 | 38 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| **Smoke Control** | | | | | | |
| CO-7104 | Smoke Control Pre-Testing | 10 | 10 | 09-Sep-14 | 22-Sep-14 | 0 |
| CO-7106 | City of Bellevue Smoke Control Testing | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 0 |
| CO-7108 | Final Marriott Smoke Control Testing | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 0 |
| **Fire Sprinklers** | | | | | | |
| CO-7110 | Fire Sprinkler Pre-Testing | 10 | 10 | 09-Sep-14 | 22-Sep-14 | 0 |

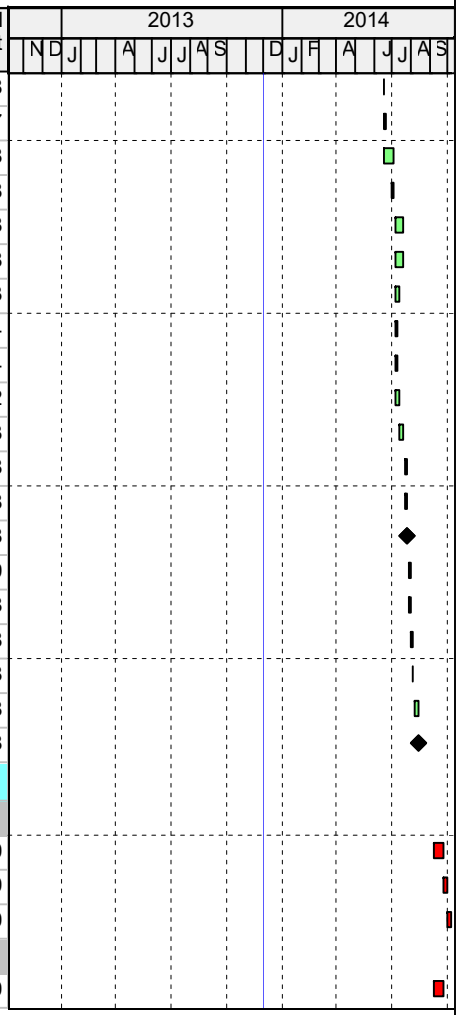



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7112 | City of Bellevue Fire Sprinkler Inspection / Approval | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 0 |
| CO-7114 | Marriott Fire Sprinkler Testing | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 0 |
| **Fire Alarm** | | | | | | |
| CO-7116 | Fire Alarm Pre-Testing | 10 | 10 | 09-Sep-14 | 19-Sep-14 | 3 |
| CO-7118 | City of Bellevue Fire Alarm Inspection / Approval | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 2 |
| CO-7120 | Marriott Fire Alarm Testing | 5 | 5 | 27-Sep-14 | 02-Oct-14 | 3 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| CO-7100 | CO - Preliminary Start-Up & Testing | 15 | 15 | 18-Aug-14 | 08-Sep-14 | 0 |
| CO-7102 | CO - HVAC Commissioning | 10 | 10 | 09-Sep-14 | 22-Sep-14 | 10 |

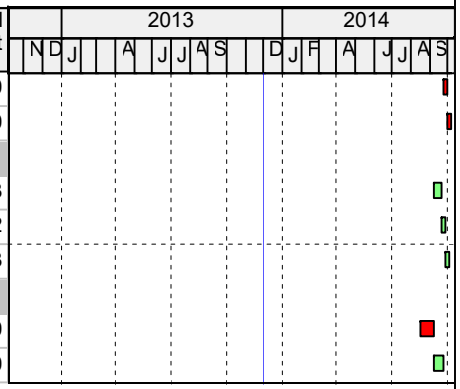



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Working Baseline Schedule 3-1-14 Update** | | | | | | |
| MM-1000 | MM - Temporary Power Available | 86 | 0 | 08-Jul-13 A | 08-Jul-13 A | |
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13 A | | |
| CM-1002 | CM - Contract Time (578 Cal Days) | 576 | 218 | 06-Mar-13 A | 05-Oct-14 | 10 |
| CM-1014 | CM - Start of Construction | 0 | 0 | 05-Apr-13 A | | |
| CM-1006 | Construction Documents Issued by Client - (Due on 7 | 0 | 0 | 02-Mar-14 | | 228 |
| CM-1008 | Finalization of Allowances - (Due on 9-2-13) | 0 | 0 | 02-Mar-14 | | 228 |
| CO-7004 | CO - Prep / Submit O&M Manuals | 40 | 40 | 31-Jul-14 | 08-Sep-14 | 37 |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 24-Aug-14* | | 0 |
| CM-1016 | CM - Owner FF+E "Build-Out" | 42 | 42 | 24-Aug-14* | 04-Oct-14 | 0 |
| CM-1018 | CM - Hotel Operations Training | 21 | 21 | 14-Sep-14* | 04-Oct-14 | 0 |
| CO-7006 | CO - Certificate of Occupancy/Substantial Completior | 0 | 0 | | 05-Oct-14 | 10 |
| CO-7122 | CO - Certificate of Occupancy | 0 | 0 | | 05-Oct-14 | 10 |
| **Misc Milestones** | | | | | | |
| CM-1020 | MM - Site Mobilization | 10 | 0 | 06-Mar-13 A | 04-Apr-13 A | |
| MM-1004 | MM - Start Drywall In Tower | 0 | 0 | 03-Apr-14 | | 196 |
| MM-1008 | MM - Top Out - Tower / Structure | 0 | 0 | | 18-Apr-14 | 180 |
| MM-1010 | Energise Permanent Power | 5 | 5 | 01-May-14 | 05-May-14 | 163 |
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 28-Aug-14 | 33 |
| **Executive Summary** | | | | | | |
| ES-1020 | Windows | 74 | 69 | 24-Feb-14 A | 06-Jun-14 | 86 |
| ES-1010 | Elevators | 115 | 115 | 22-Apr-14 | 02-Oct-14 | 9 |
| ES-1016 | Metal Wall Panels @ Podium | 10 | 10 | 12-May-14 | 23-May-14 | 25 |

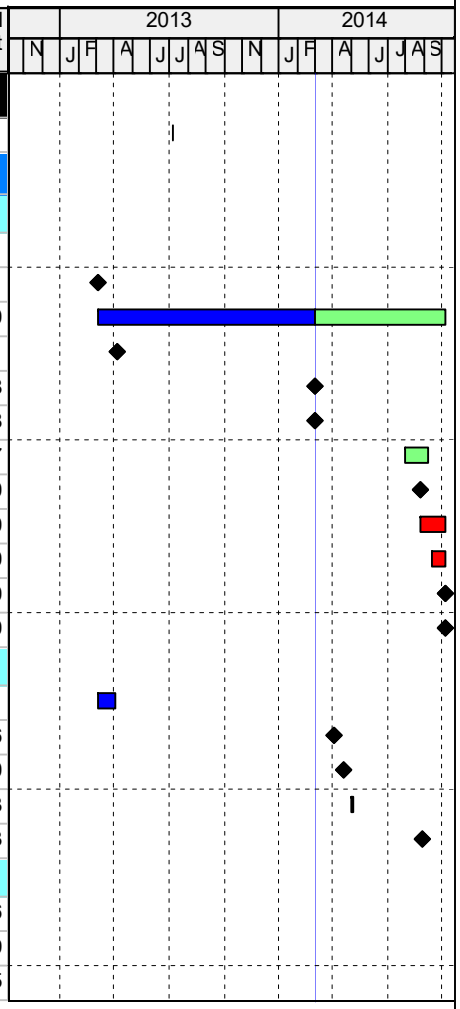


Actual Work | Remaining Work | Critical Remai... | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ES-1022 | Start-Up / Testing / Commissioning | 52 | 52 | 15-Aug-14 | 05-Oct-14 | 10 |
| ES-1024 | Curtainwall South | 10 | 10 | 02-Sep-14 | 15-Sep-14 | 22 |
| ES-1018 | Curtainwall East | 10 | 10 | 03-Sep-14 | 16-Sep-14 | 21 |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| Tower Crane | | | | | | |
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 0 | 04-Jun-13 A | 14-Jun-13 A | |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 0 | 20-Jun-13 A | 24-Jun-13 A | |
| TC-5902 | Tower Crane - Erectiion | 2 | 0 | 21-Jun-13 A | 24-Jun-13 A | |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 24-Jun-13 A | | |
| TC-5906 | Tower Crane - Operatational Period | 391 | 122 | 24-Jun-13 A | 01-Jul-14 | 105 |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 1 | 02-Jul-14 | 02-Jul-14 | 73 |
| Man & Material Lifts | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 0 | 14-Jan-14 A | 20-Jan-14 A | |
| ML-5952 | Man/Material Lifts - Erect/Build Loading Dock | 5 | 0 | 21-Jan-14 A | 27-Jan-14 A | |
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 10-Feb-14 A | | |
| ML-5954 | Man/Material Lifts - Load Test / Certify | 1 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| ML-5958 | Man/Material Lifts - Operatational Period | 196 | 176 | 10-Feb-14 A | 24-Aug-14 | 31 |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 22 |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |
| Mass Excavation / Shoring | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 0 | 05-Apr-13 A | 12-Apr-13 A | |
| SW-2002 | Demolition And Utility Relocation | 8 | 0 | 15-Apr-13 A | 19-Apr-13 A | |
| SW-2010 | Grade Subgrade for Elect/Plumbing | 3 | 0 | 07-Jan-14 A | 09-Jan-14 A | |
| Site Finishes | | | | | | |
| SW-2006 | Install Perm Power Electrical Service / Dry Utilities (Ofl | 15 | 15 | 10-Mar-14 | 28-Mar-14 | 120 |

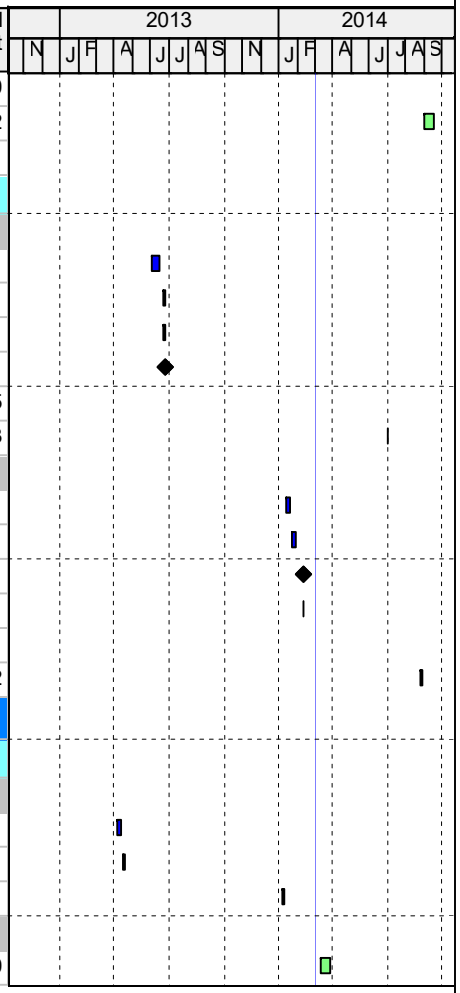


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2004 | Offsite Water & Water Connection | 5 | 5 | 31-Mar-14 | 04-Apr-14 | 135 |
| SW-2008 | Sidewalks / Landscaping / Street Improvements | 40 | 40 | 20-Aug-14 | 15-Oct-14 | 0 |
| **Structure** | | | | | | |
| **Foundation / Substructure - (Levels LL4 / LL3)** | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 0 | 12-Jun-13 A | 27-Jun-13 A | |
| LL4-1601 | LL4 - Excavate Footings | 14 | 0 | 17-Jun-13 A | 30-Jul-13 A | |
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 0 | 18-Jun-13 A | 24-Jun-13 A | |
| LL4-1606 | LL4 - Undrgmd Plumbing | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-1608 | LL4 - Undrgmd Elec | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 0 | 19-Jun-13 A | 25-Jun-13 A | |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 0 | 26-Jun-13 A | 02-Aug-13 A | |
| LL4-2033 | LL4 - Shotcrete Walls | 27 | 0 | 26-Jun-13 A | 05-Aug-13 A | |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 0 | 03-Jul-13 A | 21-Aug-13 A | |
| LL4-1614 | LL4 - FRP SOG | 5 | 0 | 10-Jul-13 A | 07-Aug-13 A | |
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 0 | 12-Jul-13 A | 26-Jul-13 A | |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 0 | 13-Jul-13 A | 06-Aug-13 A | |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 0 | 22-Jul-13 A | 24-Jul-13 A | |
| LL4-1618 | LL4 - FRP Ramp SOG | 5 | 0 | 01-Aug-13 A | 07-Aug-13 A | |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2004 | LL2 - Shore / Form Deck | 8 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2006 | LL3 - M & E Inserts | 4 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2008 | LL3 - ReSteel / PT Cables | 6 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2010 | LL3 - Install Embeds | 2 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2001 | LL3 - Waterproof Walls | 3 | 0 | 05-Aug-13 A | 05-Aug-13 A | |
| LL3-2012 | LL3 - Pour / Finish Deck | 2 | 0 | 16-Aug-13 A | 16-Aug-13 A | |
| LL3-2014 | LL3 - Stress Tendons | 1 | 0 | 19-Aug-13 A | 19-Aug-13 A | |

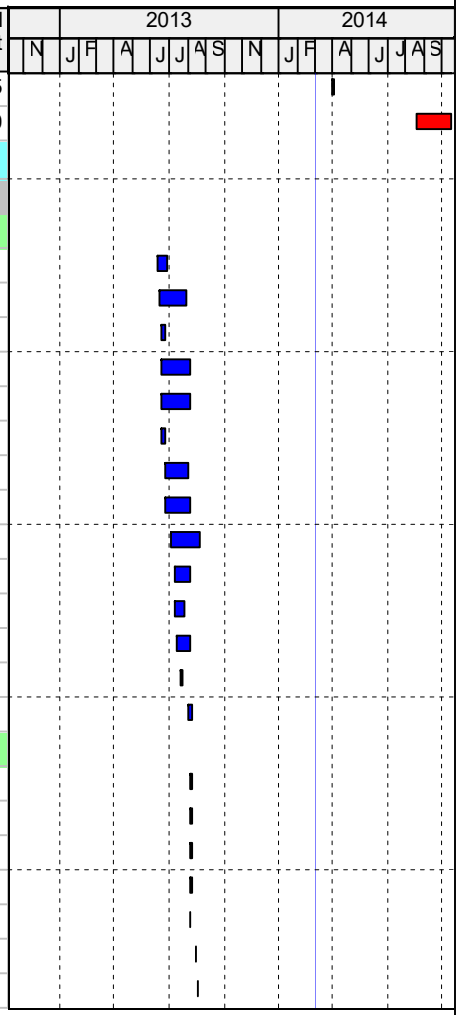



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-2000 | LL3 - FRP Core Walls | 8 | 0 | 19-Aug-13 A | 28-Aug-13 A | |
| LL3-2033 | LL3 - Shotcrete Walls | 5 | 0 | 23-Aug-13 A | 26-Aug-13 A | |
| LL3-2016 | LL3 - Strip / ReShore Deck | 3 | 0 | 01-Sep-13 A | 13-Sep-13 A | |
| LL3-2018 | LL3 - Remove ReShores | 4 | 0 | 04-Nov-13 A | 07-Nov-13 A | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Grids 1 to 4 - (SOG @ Loading Dock)** | | | | | | |
| LL2-2056 | LL2 - Grease Intercepter | 5 | 0 | 15-Aug-13 A | 21-Aug-13 A | |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 0 | 27-Aug-13 A | 04-Sep-13 A | |
| LL2-2027 | LL2 - Waterproof Walls | 2 | 0 | 27-Aug-13 A | 28-Aug-13 A | |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 0 | 30-Aug-13 A | 05-Sep-13 A | |
| LL2-2021 | LL2 - FRP Elec Vault | 14 | 0 | 30-Aug-13 A | 04-Sep-13 A | |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 0 | 04-Sep-13 A | 11-Sep-13 A | |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 0 | 11-Sep-13 A | 13-Sep-13 A | |
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls/Roof | 11 | 0 | 19-Sep-13 A | 03-Oct-13 A | |
| LL2-2020 | LL2 - Undrgmd Plumbing | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2022 | LL2 - Undrgmd Elec | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2031 | LL2 - FRP Generator SOG | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2015 | LL2 to LL1 FRP Columns / Misc Walls | 6 | 0 | 01-Oct-13 A | 01-Oct-13 A | |
| LL2-2029 | LL2 - F/R/P Pour #2 | 8 | 0 | 15-Jan-14 A | 24-Jan-14 A | |
| LL2-2011 | LL2 - F/R/P Pour #3 | 16 | 0 | 24-Jan-14 A | 18-Feb-14 A | |
| LL2-2019 | LL2 - F/R/P Pour #6 | 4 | 11 | 19-Feb-14 A | 17-Mar-14 | 109 |
| LL2-2044 | LL2 - Set Generator | 1 | 1 | 06-May-14 | 06-May-14 | 109 |
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |
| LL2-2004 | LL2 - Shore / Form Deck | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2035 | LL2 to LL1 - Shotcrete Walls | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |

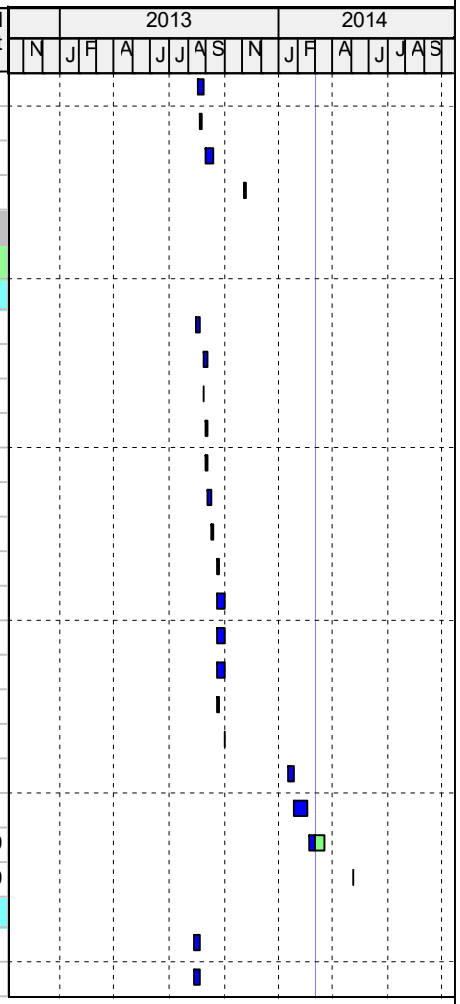



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2006 | LL2 - M & E Inserts | 4 | 0 | 14-Aug-13 A | 19-Aug-13 A | |
| LL2-2008 | LL2 - ReSteel / PT Cables | 6 | 0 | 14-Aug-13 A | 21-Aug-13 A | |
| LL2-2010 | LL2 - Install Embeds | 3 | 0 | 14-Aug-13 A | 16-Aug-13 A | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 0 | 27-Aug-13 A | 06-Sep-13 A | |
| LL2-2012 | LL2 - Place / Finish Deck | 3 | 0 | 29-Aug-13 A | 29-Aug-13 A | |
| LL2-2023 | LL2 - Waterproof Walls | 3 | 0 | 29-Aug-13 A | 03-Sep-13 A | |
| LL2-2014 | LL2 - Stress Tendons | 1 | 0 | 30-Aug-13 A | 30-Aug-13 A | |
| LL2-2016 | LL2 - Strip / ReShore | 3 | 0 | 03-Sep-13 A | 05-Sep-13 A | |
| LL2-8234 | LL2 - Place / Finish Deck | 3 | 0 | 12-Sep-13 A | 12-Sep-13 A | |
| LL2-2000 | LL2 - FRP Core Walls | 8 | 0 | 12-Sep-13 A | 23-Sep-13 A | |
| LL2-2018 | LL2 - Remove ReShores | 4 | 0 | 13-Nov-13 A | 18-Nov-13 A | |
| LL2-2013 | LL2 - F/R/P Pour #1 | 4 | 0 | 13-Jan-14 A | 16-Jan-14 A | |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| P5A-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2000 | LL1 - FRP Core Walls | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2004 | LL1 - Shore / Form Deck | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| P6-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P6-2004 | LL1 - Shore / Form Deck | 7 | 0 | 16-Sep-13 A | 24-Sep-13 A | |
| P5A-2006 | LL1 - MEP Rough In | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2008 | LL1 - ReSteel / PT Cables | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2012 | LL1 - Place / Finish Deck | 0 | 0 | 20-Sep-13 A | | |
| P5A-2020 | LL1 - Waterproof Walls | 3 | 0 | 20-Sep-13 A | 24-Sep-13 A | |
| P5A-2014 | LL1 - Stress Tendons | 1 | 0 | 23-Sep-13 A | 23-Sep-13 A | |
| P5A-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2006 | LL1 - MEP Rough In | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2008 | LL1 - ReSteel / PT Cables | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |

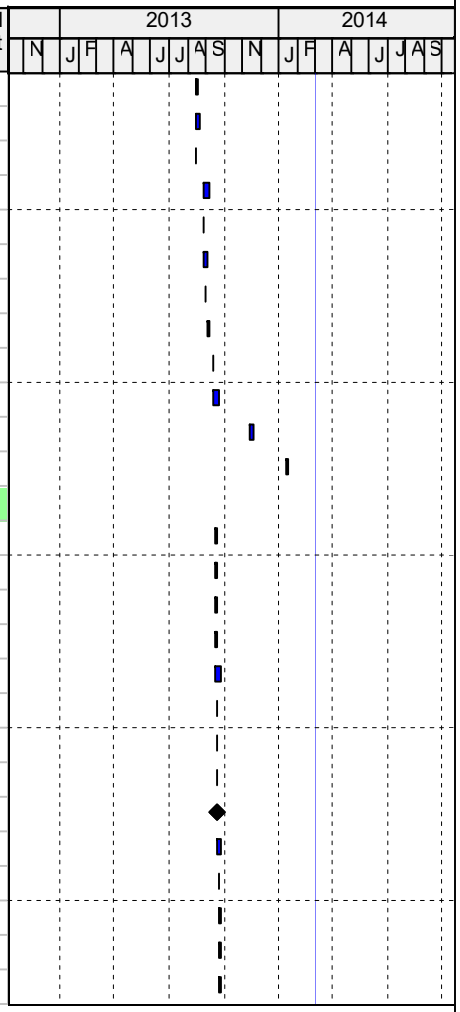



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P6-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 24-Sep-13 A | 25-Sep-13 A | |
| P6-2020 | LL1 - Waterproof Walls | 4 | 0 | 24-Sep-13 A | 27-Sep-13 A | |
| P5A-2033 | LL1 - Resteel/Shotcrete Walls | 3 | 0 | 25-Sep-13 A | 27-Sep-13 A | |
| P5B-2002 | LL1 - FRP Columns Below | 5 | 0 | 26-Sep-13 A | 02-Oct-13 A | |
| P5B-2004 | LL1 - Shore / Form Deck | 7 | 0 | 26-Sep-13 A | 04-Oct-13 A | |
| P6-2012 | LL1 - Place / Finish Deck | 0 | 0 | 27-Sep-13 A | | |
| P6-2014 | LL1 - Stress Tendons | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2033 | LL1 - Resteel/Shotcrete Walls | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 01-Oct-13 A | 03-Oct-13 A | |
| P5B-2006 | LL1 - MEP Rough In | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2002 | FRP Columns Below | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2004 | Shore / Form Deck | 4 | 0 | 03-Oct-13 A | 08-Oct-13 A | |
| P5B-2008 | LL1 - ReSteel / PT Cables | 5 | 0 | 04-Oct-13 A | 10-Oct-13 A | |
| P5B-2010 | LL1 - Install Edgeform/Embeds | 4 | 0 | 04-Oct-13 A | 09-Oct-13 A | |
| P8-2002 | FRP Columns Below | 5 | 0 | 07-Oct-13 A | 11-Oct-13 A | |
| P8-2000 | Form/Resteel/Close Core Walls | 14 | 0 | 07-Oct-13 A | 24-Oct-13 A | |
| P8-2004 | Shore / Form Deck P8 | 8 | 0 | 07-Oct-13 A | 16-Oct-13 A | |
| P7-2002 | FRP Columns Below | 5 | 0 | 08-Oct-13 A | 14-Oct-13 A | |
| P7-2004 | Shore / Form Deck | 6 | 0 | 08-Oct-13 A | 15-Oct-13 A | |
| P10A--2006 | MEP Rough In | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2008 | ReSteel / PT Cables | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2010 | Install Edgeform/Embeds | 2 | 0 | 08-Oct-13 A | 09-Oct-13 A | |
| P5B-2012 | LL1 - Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P10A--2012 | Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P5B-2014 | LL1 - Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P7-2006 | MEP Rough In | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P7-2008 | ReSteel / PT Cables | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |

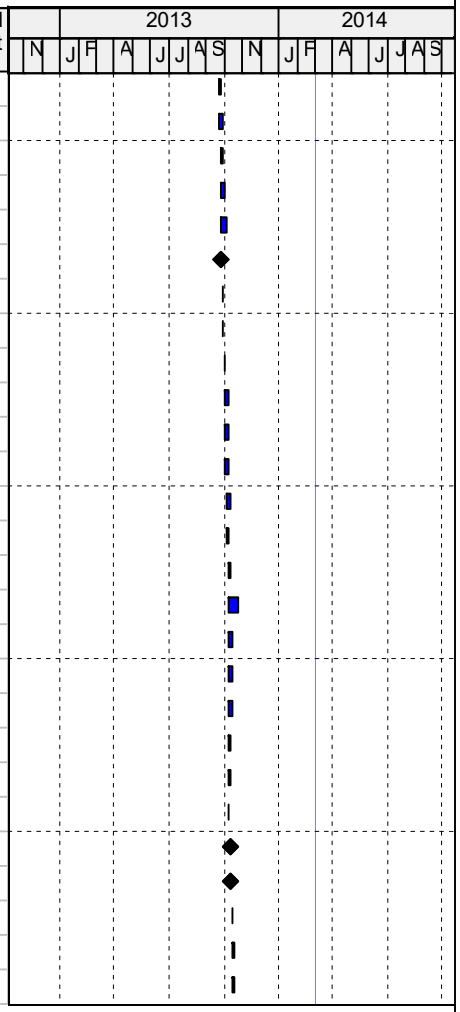


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P10A--2014 | Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P8-2020 | Shore / Form Deck P9 | 6 | 0 | 14-Oct-13 A | 21-Oct-13 A | |
| P5B-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2010 | Install Edgeform/Embeds | 2 | 0 | 15-Oct-13 A | 16-Oct-13 A | |
| P8-2006 | MEP Rough In | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2008 | ReSteel / PT Cables | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2010 | Install Edgeform/Embeds | 4 | 0 | 15-Oct-13 A | 18-Oct-13 A | |
| P10A--2016 | Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2012 | Place / Finish Deck | 0 | 0 | 18-Oct-13 A | | |
| P7-2033 | Resteel/Shotcrete Walls | 3 | 0 | 18-Oct-13 A | 22-Oct-13 A | |
| P7-2014 | Stress Tendons | 1 | 0 | 21-Oct-13 A | 21-Oct-13 A | |
| P7-2016 | Strip / ReShore Deck | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2002 | FRP Columns Below | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P10B--2000 | FRP Shear Walls Below | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2004 | Shore / Form Deck | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P8-2012 | Place / Finish Deck P 8 & 9 and Core Walls | 0 | 0 | 25-Oct-13 A | | |
| P8-2014 | Stress Tendons | 1 | 0 | 28-Oct-13 A | 28-Oct-13 A | |
| P10B--2006 | MEP Rough In | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2008 | ReSteel / PT Cables | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2010 | Install Edgeform/Embeds | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P12--2002 | FRP Columns Below | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P12--2000 | Form/Resteel/Close Core Walls | 9 | 0 | 28-Oct-13 A | 07-Nov-13 A | |
| P12--2004 | Shore / Form Deck | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P8-2016 | Strip / ReShore Deck | 3 | 0 | 29-Oct-13 A | 31-Oct-13 A | |
| P11--2002 | FRP Columns Below | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P11--2004 | Shore / Form Deck | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P10B--2012 | Place / Finish Deck | 0 | 0 | 31-Oct-13 A | | |

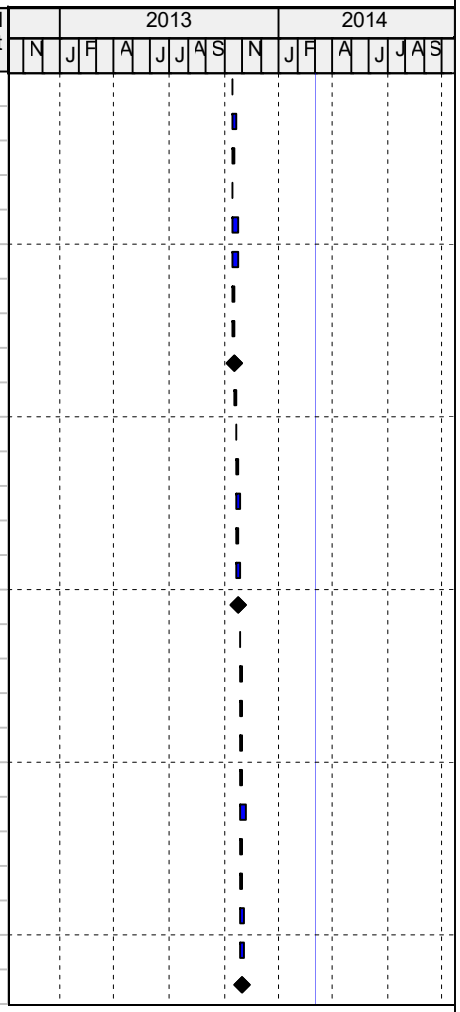



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P10B–2014 | Stress Tendons | 1 | 0 | 01-Nov-13 A | 01-Nov-13 A | |
| P12–2006 | MEP Rough In | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12–2008 | ReSteel / PT Cables | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12–2010 | Install Edgeform/Embeds | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P10B–2016 | Strip / ReShore Deck | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2006 | MEP Rough In | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2008 | ReSteel / PT Cables | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2010 | Install Edgeform/Embeds | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2012 | Place / Finish Deck | 0 | 0 | 07-Nov-13 A | | |
| P13–2002 | FRP Columns Below | 5 | 0 | 07-Nov-13 A | 14-Nov-13 A | |
| P13–2004 | Shore / Form Deck | 9 | 0 | 07-Nov-13 A | 28-Nov-13 A | |
| P11–2014 | Stress Tendons | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| P12–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 08-Nov-13 A | | |
| P11–2016 | Strip / ReShore Deck | 3 | 0 | 12-Nov-13 A | 14-Nov-13 A | |
| P12–2014 | Stress Tendons | 1 | 0 | 12-Nov-13 A | 12-Nov-13 A | |
| P14–2002 | FRP Columns Below | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P14–2000 | Form/Resteel/Close Core Walls | 8 | 0 | 19-Nov-13 A | 03-Dec-13 A | |
| P14–2004 | Shore / Form Deck | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P13A–2002 | FRP Columns Below | 5 | 0 | 21-Nov-13 A | 27-Nov-13 A | |
| P13A–2004 | Shore / Form Deck | 4 | 0 | 21-Nov-13 A | 26-Nov-13 A | |
| P13–2010 | Install Edgeform/Embeds | 5 | 0 | 22-Nov-13 A | 04-Dec-13 A | |
| P13–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2006 | MEP Rough In | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2010 | Install Edgeform/Embeds | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P13–2006 | MEP Rough In | 5 | 0 | 26-Nov-13 A | 03-Dec-13 A | |
| P13A–2006 | MEP Rough In | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |

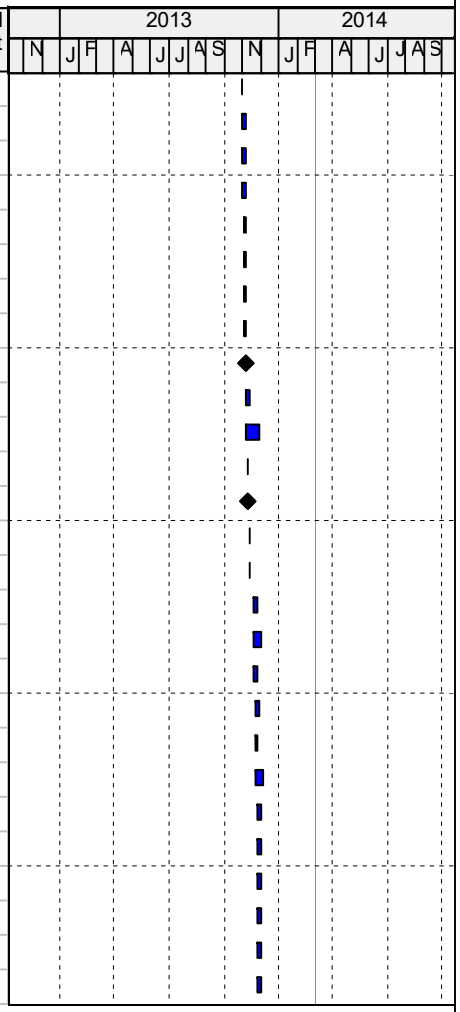



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P13A–2008 | ReSteel / PT Cables | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2010 | Install Edgeform/Embeds | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13–2012 | Place / Finish Deck | 0 | 0 | 02-Dec-13 A | | |
| P13A–2012 | Place / Finish Deck | 0 | 0 | 03-Dec-13 A | | |
| P14–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 04-Dec-13 A | | |
| P13–2014 | Stress Tendons | 1 | 0 | 05-Dec-13 A | 05-Dec-13 A | |
| P15–2002 | FRP Columns Below | 3 | 0 | 05-Dec-13 A | 09-Dec-13 A | |
| P15–2000 | Jump/Resteel/Close Core | 9 | 0 | 05-Dec-13 A | 17-Dec-13 A | |
| P15–2004 | Shore / Form Deck | 5 | 0 | 05-Dec-13 A | 11-Dec-13 A | |
| P13–2016 | Strip / ReShore Deck | 3 | 0 | 06-Dec-13 A | 10-Dec-13 A | |
| P13A–2014 | Stress Tendons | 1 | 0 | 06-Dec-13 A | 06-Dec-13 A | |
| P14–2014 | Stress Tendons | 1 | 0 | 07-Dec-13 A | 07-Dec-13 A | |
| P15–2006 | MEP Rough In | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2008 | ReSteel / PT Cables | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2010 | Install Edgeform/Embeds | 3 | 0 | 11-Dec-13 A | 13-Dec-13 A | |
| P16-2002 | FRP Columns Below | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P16-2004 | Shore / Form Deck | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P15–2012 | Place / Finish Deck | 0 | 0 | 18-Dec-13 A | | |
| P15–2020 | Place Conc @ Core | 0 | 0 | 18-Dec-13 A | | |
| P16-2000 | Jump/Resteel/Close Core | 5 | 0 | 18-Dec-13 A | 24-Dec-13 A | |
| P16-2006 | MEP Rough In | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2008 | ReSteel / PT Cables | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2010 | Install Edgeform/Embeds | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P15–2014 | Stress Tendons | 1 | 0 | 21-Dec-13 A | 21-Dec-13 A | |
| P8-2018 | Remove Reshores | 2 | 0 | 23-Dec-13 A | 24-Dec-13 A | |
| P10A–2018 | Remove Reshores | 2 | 0 | 26-Dec-13 A | 27-Dec-13 A | |
| P16-2012 | Place / Finish Deck | 0 | 0 | 26-Dec-13 A | | |

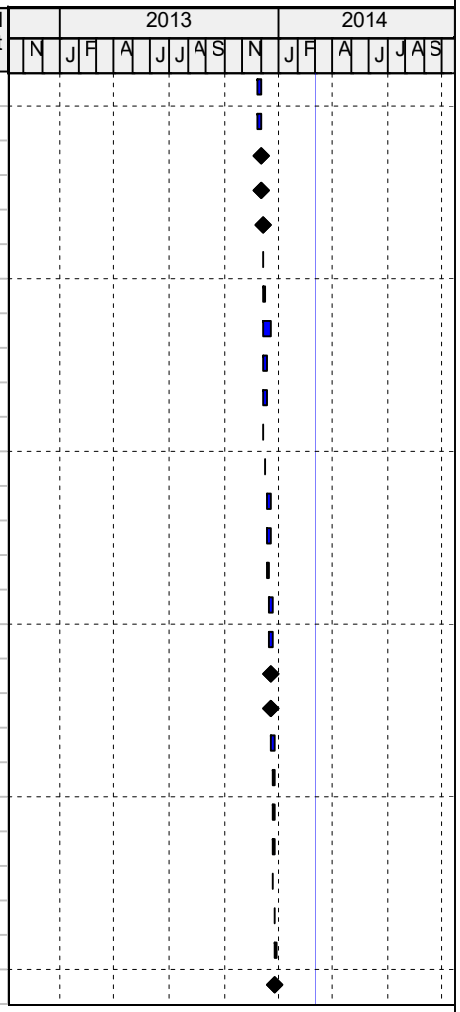



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P16-2020 | Place Conc @ Core | 0 | 0 | 26-Dec-13 A | | |
| P17-2002 | FRP Columns Below | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P17-2000 | Jump/Resteel/Close Core | 7 | 0 | 27-Dec-13 A | 07-Jan-14 A | |
| P17-2004 | Shore / Form Deck | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P10B--2018 | Remove Reshores | 2 | 0 | 30-Dec-13 A | 31-Dec-13 A | |
| P16-2014 | Stress Tendons | 1 | 0 | 31-Dec-13 A | 31-Dec-13 A | |
| P5A-2018 | LL1 - Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P11--2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P12--2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P17-2006 | MEP Rough In | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2008 | ReSteel / PT Cables | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2010 | Install Edgeform/Embeds | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P6-2018 | LL1 - Remove Reshores | 2 | 0 | 06-Jan-14 A | 07-Jan-14 A | |
| P5B-2018 | LL1 - Remove Reshores | 2 | 0 | 08-Jan-14 A | 09-Jan-14 A | |
| P17-2012 | Place / Finish Deck | 0 | 0 | 08-Jan-14 A | | |
| P17-2020 | Place Conc @ Core | 0 | 0 | 08-Jan-14 A | | |
| P18-2002 | FRP Columns Below | 5 | 0 | 09-Jan-14 A | 15-Jan-14 A | |
| P18-2000 | Jump/Resteel/Close Core | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P18-2004 | Shore / Form Deck | 3 | 0 | 09-Jan-14 A | 13-Jan-14 A | |
| LL2-2022R | MEP Rough In | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P7-2018 | Remove Reshores | 2 | 0 | 10-Jan-14 A | 13-Jan-14 A | |
| P17-2014 | Stress Tendons | 1 | 0 | 11-Jan-14 A | 11-Jan-14 A | |
| P13--2018 | Remove Reshores | 2 | 0 | 13-Jan-14 A | 14-Jan-14 A | |
| P13A--2018 | Remove Reshores | 2 | 0 | 15-Jan-14 A | 16-Jan-14 A | |
| WEA-2012 | WIND IMPACT | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| P18-2006 | MEP Rough In | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2008 | ReSteel / PT Cables | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |

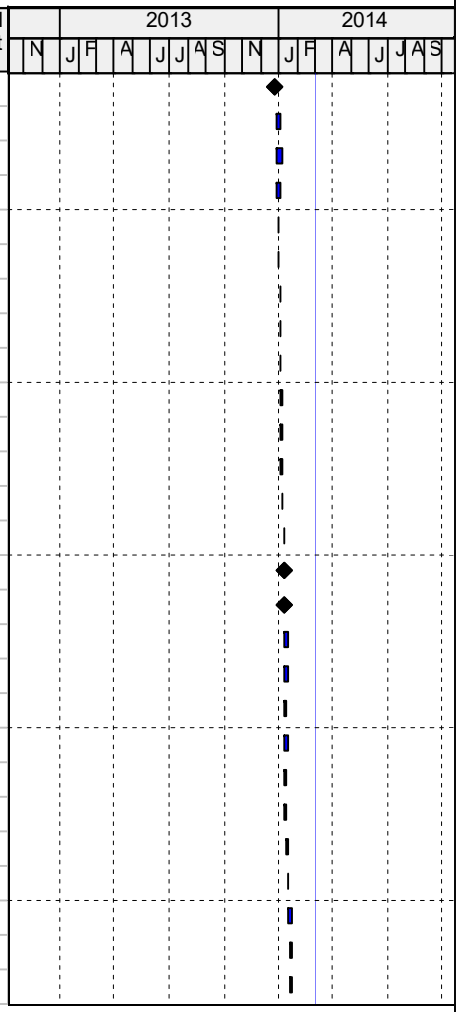



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P18-2010 | Install Edgeform/Embeds | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2012 | Place / Finish Deck | 0 | 0 | 22-Jan-14 A | | |
| P18-2020 | Place Conc @ Core | 0 | 0 | 22-Jan-14 A | | |
| P19-2002 | FRP Columns Below | 5 | 0 | 23-Jan-14 A | 29-Jan-14 A | |
| P19-2000 | Jump/Resteel/Close Core | 4 | 0 | 23-Jan-14 A | 28-Jan-14 A | |
| P19-2004 | Shore / Form Deck | 3 | 0 | 23-Jan-14 A | 27-Jan-14 A | |
| P18-2014 | Stress Tendons | 1 | 0 | 25-Jan-14 A | 25-Jan-14 A | |
| P14–2018 | Remove Reshores | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2006 | MEP Rough In | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2008 | ReSteel / PT Cables | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2010 | Install Edgeform/Embeds | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2012 | Place / Finish Deck | 0 | 0 | 29-Jan-14 A | | |
| P19-2020 | Place Conc @ Core | 0 | 0 | 29-Jan-14 A | | |
| P20-2002 | FRP Columns Below | 5 | 0 | 30-Jan-14 A | 05-Feb-14 A | |
| P20-2000 | Jump/Resteel/Close Core | 9 | 0 | 30-Jan-14 A | 11-Feb-14 A | |
| P20-2004 | Shore / Form Deck | 6 | 0 | 30-Jan-14 A | 10-Feb-14 A | |
| P19-2014 | Stress Tendons | 1 | 0 | 01-Feb-14 A | 01-Feb-14 A | |
| P13A–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P14–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P15–2016 | Strip / ReShore Deck | 3 | 0 | 06-Feb-14 A | 10-Feb-14 A | |
| P20-2006 | MEP Rough In | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2008 | ReSteel / PT Cables | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2010 | Install Edgeform/Embeds | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| L03-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 06-Feb-14 A | 12-Feb-14 A | |
| P16-2016 | Strip / ReShore Deck | 3 | 0 | 10-Feb-14 A | 12-Feb-14 A | |
| L04-2018 | Remove Reshores | 2 | 0 | 10-Feb-14 A | 11-Feb-14 A | |
| L03-2018 | Remove Reshores | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |

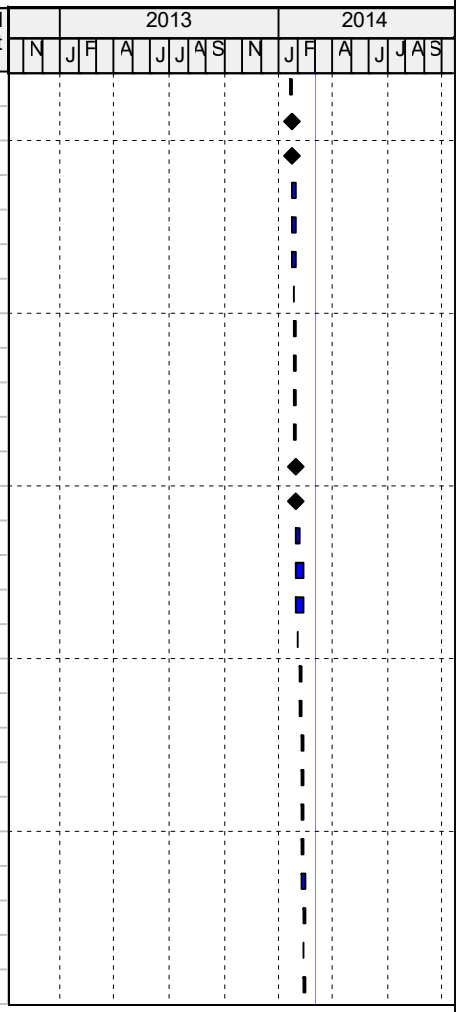



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P17-2016 | Strip / ReShore Deck | 3 | 0 | 12-Feb-14 A | 14-Feb-14 A | |
| P20-2012 | Place / Finish Deck | 0 | 0 | 12-Feb-14 A | | |
| P20-2020 | Place Conc @ Core | 0 | 0 | 12-Feb-14 A | | |
| L04-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-Feb-14 A | 18-Feb-14 A | |
| P12–2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P18-2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P21-2002 | FRP Columns Below | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| P21-2000 | Jump/Resteel/Close Core | 4 | 0 | 13-Feb-14 A | 18-Feb-14 A | |
| P21-2004 | Shore / Form Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P19-2016 | Strip / ReShore Deck | 3 | 0 | 14-Feb-14 A | 18-Feb-14 A | |
| P20-2014 | Stress Tendons | 1 | 0 | 15-Feb-14 A | 15-Feb-14 A | |
| P21-2006 | MEP Rough In | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2008 | ReSteel / PT Cables | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P20-2016 | Strip / ReShore Deck | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| L05-2018 | Remove Reshores | 2 | 0 | 18-Feb-14 A | 19-Feb-14 A | |
| P21-2012 | Place / Finish Deck | 0 | 0 | 19-Feb-14 A | | |
| P21-2020 | Place Conc @ Core | 0 | 0 | 19-Feb-14 A | | |
| P22-2002 | FRP Columns Below | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P22-2000 | Jump/Resteel/Close Core | 4 | 0 | 20-Feb-14 A | 25-Feb-14 A | |
| P22-2004 | Shore / Form Deck | 3 | 0 | 20-Feb-14 A | 24-Feb-14 A | |
| L05-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P21-2014 | Stress Tendons | 1 | 0 | 22-Feb-14 A | 22-Feb-14 A | |
| P21-2016 | Strip / ReShore Deck | 3 | 0 | 24-Feb-14 A | 26-Feb-14 A | |
| P22-2006 | MEP Rough In | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2008 | ReSteel / PT Cables | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |

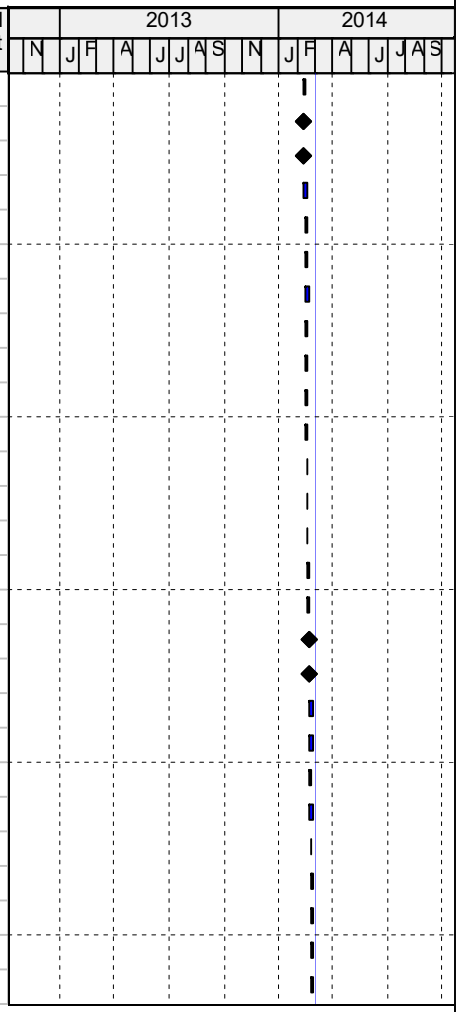



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-2018 | Remove Reshores | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| P22-2012 | Place / Finish Deck | 0 | 0 | 26-Feb-14 A | | |
| P22-2020 | Place Conc @ Core | 0 | 0 | 26-Feb-14 A | | |
| P23-2002 | FRP Columns Below | 4 | 3 | 27-Feb-14 A | 05-Mar-14 | 157 |
| P23-2000 | Jump/Resteel/Close Core | 4 | 2 | 27-Feb-14 A | 04-Mar-14 | 158 |
| P23-2004 | Shore / Form Deck | 3 | 1 | 27-Feb-14 A | 03-Mar-14 | 9 |
| L06-2019 | Grind Ceiling for Skim Coat | 5 | 3 | 27-Feb-14 A | 05-Mar-14 | 17 |
| P22-2014 | Stress Tendons | 1 | 0 | 01-Mar-14 A | 01-Mar-14 A | |
| P22-2016 | Strip / ReShore Deck | 3 | 3 | 03-Mar-14 | 05-Mar-14 | 30 |
| P23-2006 | MEP Rough In | 2 | 2 | 03-Mar-14 | 04-Mar-14 | 9 |
| P23-2008 | ReSteel / PT Cables | 2 | 2 | 03-Mar-14 | 04-Mar-14 | 9 |
| P23-2010 | Install Edgeform/Embeds | 2 | 2 | 03-Mar-14 | 04-Mar-14 | 9 |
| L07-2018 | Remove Reshores | 2 | 2 | 04-Mar-14 | 05-Mar-14 | 17 |
| P23-2012 | Place / Finish Deck | 0 | 0 | 05-Mar-14 | | 9 |
| P23-2020 | Place Conc @ Core | 0 | 0 | 05-Mar-14 | | 158 |
| P24-2002 | FRP Columns Below | 5 | 5 | 06-Mar-14 | 12-Mar-14 | 152 |
| P24-2000 | Jump/Resteel/Close Core | 4 | 4 | 06-Mar-14 | 11-Mar-14 | 153 |
| P24-2004 | Shore / Form Deck | 3 | 3 | 06-Mar-14 | 10-Mar-14 | 9 |
| L07-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 06-Mar-14 | 12-Mar-14 | 17 |
| P23-2014 | Stress Tendons | 1 | 1 | 08-Mar-14 | 08-Mar-14 | 23 |
| P23-2016 | Strip / ReShore Deck | 3 | 3 | 10-Mar-14 | 12-Mar-14 | 30 |
| P24-2006 | MEP Rough In | 2 | 2 | 10-Mar-14 | 11-Mar-14 | 9 |
| P24-2008 | ReSteel / PT Cables | 2 | 2 | 10-Mar-14 | 11-Mar-14 | 9 |
| P24-2010 | Install Edgeform/Embeds | 2 | 2 | 10-Mar-14 | 11-Mar-14 | 9 |
| L08-2018 | Remove Reshores | 2 | 2 | 11-Mar-14 | 12-Mar-14 | 17 |
| P24-2012 | Place / Finish Deck | 0 | 0 | 12-Mar-14 | | 9 |
| P24-2020 | Place Conc @ Core | 0 | 0 | 12-Mar-14 | | 153 |

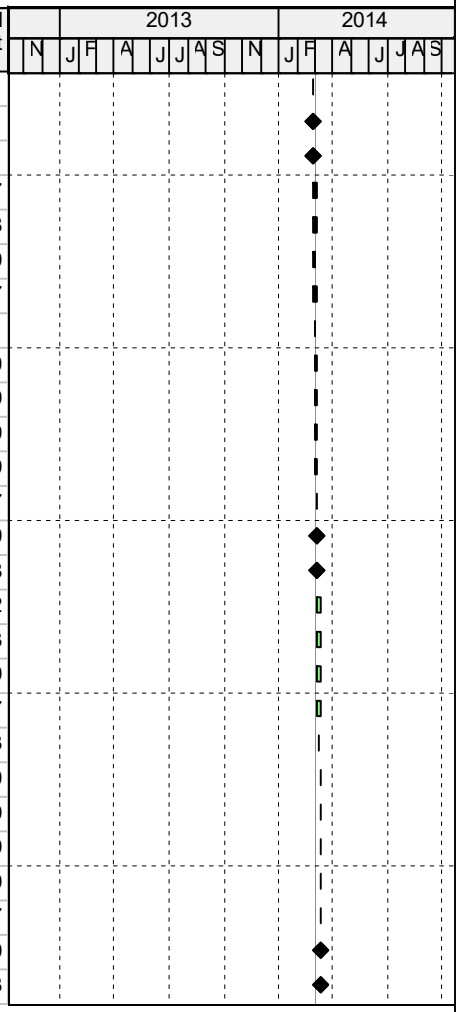



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P25-2002 | FRP Columns Below | 5 | 5 | 13-Mar-14 | 19-Mar-14 | 147 |
| P25-2000 | Jump/Resteel/Close Core | 4 | 4 | 13-Mar-14 | 18-Mar-14 | 148 |
| P25-2004 | Shore / Form Deck | 3 | 3 | 13-Mar-14 | 17-Mar-14 | 9 |
| L08-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 13-Mar-14 | 19-Mar-14 | 17 |
| P24-2014 | Stress Tendons | 1 | 1 | 15-Mar-14 | 15-Mar-14 | 23 |
| P24-2016 | Strip / ReShore Deck | 3 | 3 | 17-Mar-14 | 19-Mar-14 | 39 |
| P25-2006 | MEP Rough In | 2 | 2 | 17-Mar-14 | 18-Mar-14 | 9 |
| P25-2008 | ReSteel / PT Cables | 2 | 2 | 17-Mar-14 | 18-Mar-14 | 9 |
| P25-2010 | Install Edgeform/Embeds | 2 | 2 | 17-Mar-14 | 18-Mar-14 | 9 |
| L09-2018 | Remove Reshores | 2 | 2 | 18-Mar-14 | 19-Mar-14 | 17 |
| P25-2012 | Place / Finish Deck | 0 | 0 | 19-Mar-14 | | 9 |
| P25-2020 | Place Conc @ Core | 0 | 0 | 19-Mar-14 | | 148 |
| P26-2002 | FRP Columns Below | 5 | 5 | 20-Mar-14 | 26-Mar-14 | 142 |
| P26-2000 | Jump/Resteel/Close Core | 4 | 4 | 20-Mar-14 | 25-Mar-14 | 143 |
| P26-2004 | Shore / Form Deck | 3 | 3 | 20-Mar-14 | 24-Mar-14 | 9 |
| L09-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 20-Mar-14 | 26-Mar-14 | 17 |
| P25-2014 | Stress Tendons | 1 | 1 | 22-Mar-14 | 22-Mar-14 | 23 |
| P26-2006 | MEP Rough In | 2 | 2 | 24-Mar-14 | 25-Mar-14 | 9 |
| P26-2008 | ReSteel / PT Cables | 2 | 2 | 24-Mar-14 | 25-Mar-14 | 9 |
| P26-2010 | Install Edgeform/Embeds | 2 | 2 | 24-Mar-14 | 25-Mar-14 | 9 |
| P25-2016 | Strip / ReShore Deck | 3 | 3 | 24-Mar-14 | 26-Mar-14 | 38 |
| P26-2012 | Place / Finish Deck | 0 | 0 | 26-Mar-14 | | 9 |
| P26-2020 | Place Conc @ Core | 0 | 0 | 26-Mar-14 | | 143 |
| L10-2018 | Remove Reshores | 2 | 2 | 26-Mar-14 | 27-Mar-14 | 16 |
| P27-2002 | FRP Columns Below | 5 | 5 | 27-Mar-14 | 02-Apr-14 | 137 |
| P27-2000 | Jump/Resteel/Close Core | 4 | 4 | 27-Mar-14 | 01-Apr-14 | 138 |
| P27-2004 | Shore / Form Deck | 3 | 3 | 27-Mar-14 | 31-Mar-14 | 9 |

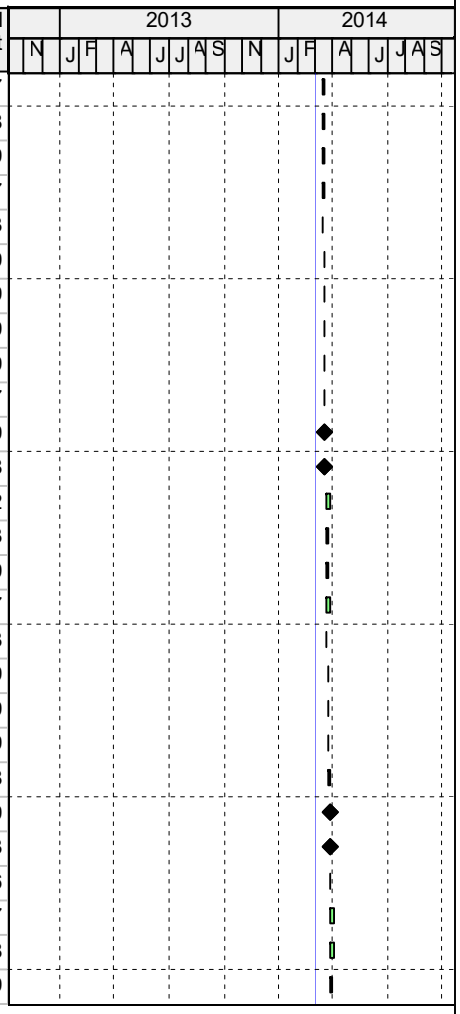



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 28-Mar-14 | 03-Apr-14 | 16 |
| P26-2014 | Stress Tendons | 1 | 1 | 29-Mar-14 | 29-Mar-14 | 22 |
| P27-2006 | MEP Rough In | 2 | 2 | 31-Mar-14 | 01-Apr-14 | 9 |
| P27-2008 | ReSteel / PT Cables | 2 | 2 | 31-Mar-14 | 01-Apr-14 | 9 |
| P27-2010 | Install Edgeform/Embeds | 2 | 2 | 31-Mar-14 | 01-Apr-14 | 9 |
| P26-2016 | Strip / ReShore Deck | 3 | 3 | 31-Mar-14 | 02-Apr-14 | 35 |
| L11-2018 | Remove Reshores | 2 | 2 | 01-Apr-14 | 02-Apr-14 | 17 |
| P27-2012 | Place / Finish Deck | 0 | 0 | 02-Apr-14 | | 9 |
| P27-2020 | Place Conc @ Core | 0 | 0 | 02-Apr-14 | | 138 |
| P28-2002 | FRP Columns Below | 5 | 5 | 03-Apr-14 | 09-Apr-14 | 132 |
| P28-2000 | Jump/Resteel/Close Core | 9 | 9 | 03-Apr-14 | 15-Apr-14 | 126 |
| P28-2004 | Shore / Form Deck | 6 | 6 | 03-Apr-14 | 10-Apr-14 | 9 |
| L11-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 03-Apr-14 | 09-Apr-14 | 17 |
| P27-2014 | Stress Tendons | 1 | 1 | 05-Apr-14 | 05-Apr-14 | 23 |
| P27-2016 | Strip / ReShore Deck | 3 | 3 | 07-Apr-14 | 09-Apr-14 | 32 |
| P28-2006 | MEP Rough In | 4 | 4 | 10-Apr-14 | 15-Apr-14 | 9 |
| P28-2008 | ReSteel / PT Cables | 4 | 4 | 10-Apr-14 | 15-Apr-14 | 9 |
| P28-2010 | Install Edgeform/Embeds | 2 | 2 | 10-Apr-14 | 11-Apr-14 | 11 |
| L12-2018 | Remove Reshores | 2 | 2 | 15-Apr-14 | 16-Apr-14 | 21 |
| P28-2012 | Place / Finish Deck | 0 | 0 | 16-Apr-14 | | 9 |
| P28-2020 | Place Conc @ Core | 0 | 0 | 16-Apr-14 | | 126 |
| P29-2002 | FRP Columns Above Roof Deck | 3 | 3 | 16-Apr-14 | 18-Apr-14 | 9 |
| P29-2000 | Strip Core | 2 | 2 | 16-Apr-14 | 17-Apr-14 | 126 |
| L12-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 17-Apr-14 | 23-Apr-14 | 21 |
| L14-2018 | Remove Reshores | 2 | 2 | 17-Apr-14 | 18-Apr-14 | 23 |
| P28-2014 | Stress Tendons | 1 | 1 | 19-Apr-14 | 19-Apr-14 | 29 |
| P28-2016 | Strip / ReShore Deck | 3 | 3 | 21-Apr-14 | 23-Apr-14 | 36 |

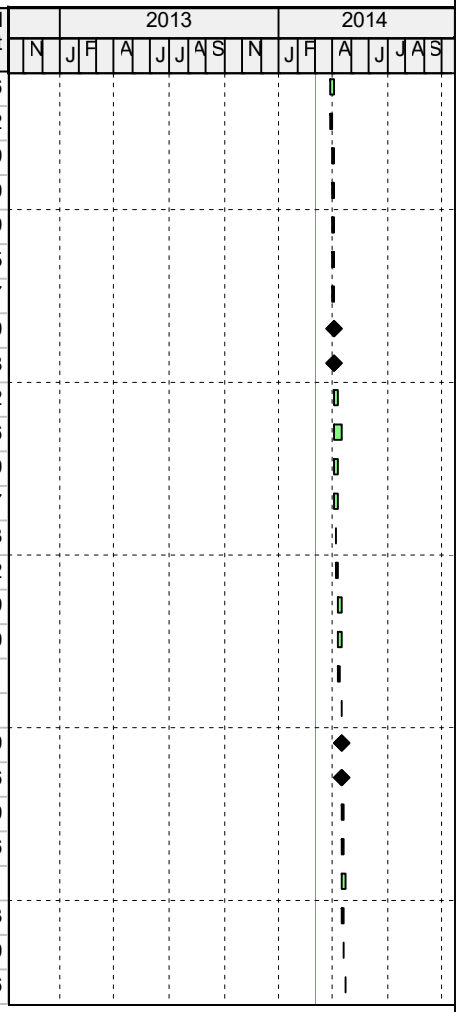



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 21-Apr-14 | 25-Apr-14 | 23 |
| L15-2018 | Remove Reshores | 2 | 2 | 21-Apr-14 | 22-Apr-14 | 23 |
| L15-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 23-Apr-14 | 29-Apr-14 | 23 |
| L16-2018 | Remove Reshores | 2 | 2 | 23-Apr-14 | 24-Apr-14 | 23 |
| L16-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 25-Apr-14 | 01-May-14 | 23 |
| L17-2018 | Remove Reshores | 2 | 2 | 25-Apr-14 | 28-Apr-14 | 35 |
| L17-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 29-Apr-14 | 05-May-14 | 35 |
| **Ballroom Catwalk & Roof** | | | | | | |
| PC-2100 | Erect Structural Steel @ Porte Cochere | 3 | 0 | 30-Jan-14 A | 03-Feb-14 A | |
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 7 | 0 | 07-Feb-14 A | 17-Feb-14 A | |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| PC-2102 | Metal Decking @ Porte Cochere/ Roof | 2 | 2 | 03-Mar-14 | 04-Mar-14 | 51 |
| BR-2112 | BR - Fireproofing @ Structural Steel | 5 | 5 | 02-May-14 | 08-May-14 | 13 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Mech Penthouse** | | | | | | |
| PH-8702 | PH - Structural Steel / Decking / Framing | 10 | 10 | 21-Apr-14 | 02-May-14 | 9 |
| PH-8706 | Set Mech Equipment @ Tower Roof | 2 | 2 | 05-May-14 | 06-May-14 | 112 |
| PH-8708 | Set Equipment @ Penthouse | 3 | 3 | 05-May-14 | 07-May-14 | 73 |
| PH-8700 | High Roof - Structural Steel | 10 | 10 | 08-May-14 | 21-May-14 | 73 |
| **Vertical Circulation** | | | | | | |
| **Stairs** | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 25-Nov-13 A | 26-Nov-13 A | |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 27-Nov-13 A | 03-Dec-13 A | |
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 04-Dec-13 A | 05-Dec-13 A | |
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 06-Dec-13 A | 09-Dec-13 A | |
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 2 | 0 | 03-Feb-14 A | 04-Feb-14 A | |

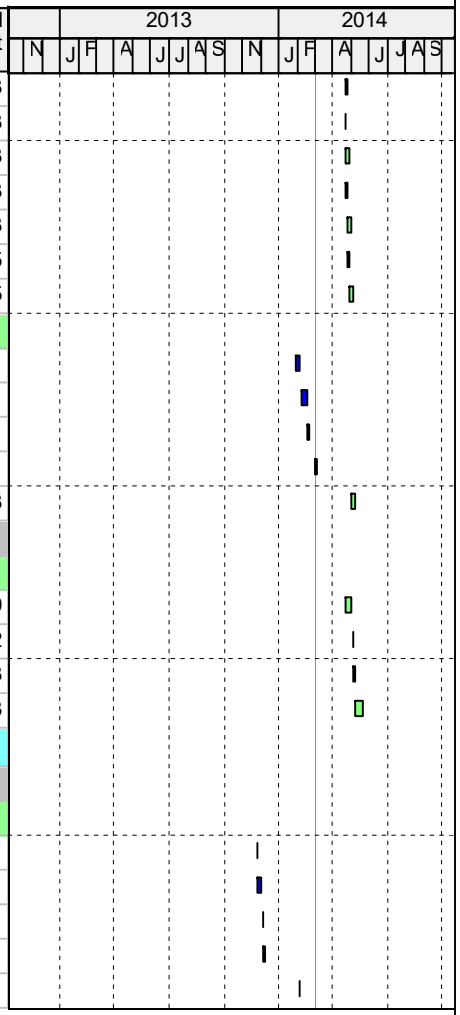



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 2 | 0 | 07-Feb-14 A | 10-Feb-14 A | |
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 2 | 2 | 12-Mar-14 | 13-Mar-14 | 113 |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 2 | 2 | 14-Mar-14 | 17-Mar-14 | 113 |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 2 | 2 | 18-Mar-14 | 19-Mar-14 | 113 |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 2 | 2 | 20-Mar-14 | 21-Mar-14 | 113 |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 2 | 2 | 16-Apr-14 | 17-Apr-14 | 96 |
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 2 | 2 | 18-Apr-14 | 21-Apr-14 | 96 |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 2 | 2 | 22-Apr-14 | 23-Apr-14 | 96 |
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 2 | 2 | 24-Apr-14 | 25-Apr-14 | 96 |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 2 | 2 | 28-Apr-14 | 29-Apr-14 | 104 |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 2 | 2 | 12-May-14 | 13-May-14 | 96 |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 2 | 2 | 14-May-14 | 15-May-14 | 96 |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 2 | 2 | 16-May-14 | 19-May-14 | 96 |
| S1-4040 | Stair 1 - Set Mtl Stairs / Railings L18 | 2 | 2 | 20-May-14 | 21-May-14 | 96 |
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 10-Dec-13 A | 11-Dec-13 A | |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 12-Dec-13 A | 13-Dec-13 A | |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 16-Dec-13 A | 17-Dec-13 A | |
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 18-Dec-13 A | 19-Dec-13 A | |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 2 | 0 | 13-Feb-14 A | 14-Feb-14 A | |
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 2 | 0 | 19-Feb-14 A | 20-Feb-14 A | |
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 2 | 0 | 21-Feb-14 A | 24-Feb-14 A | |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 2 | 2 | 24-Mar-14 | 25-Mar-14 | 113 |
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 2 | 2 | 26-Mar-14 | 27-Mar-14 | 113 |

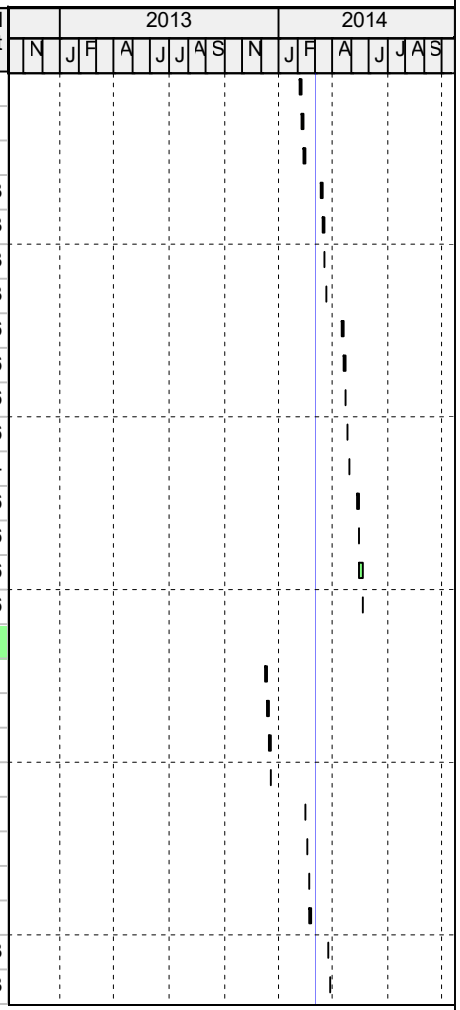



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 2 | 2 | 28-Mar-14 | 31-Mar-14 | 113 |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 2 | 2 | 01-Apr-14 | 02-Apr-14 | 113 |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 2 | 2 | 28-Apr-14 | 29-Apr-14 | 96 |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 2 | 2 | 30-Apr-14 | 01-May-14 | 96 |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 2 | 2 | 02-May-14 | 05-May-14 | 96 |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 2 | 2 | 06-May-14 | 07-May-14 | 96 |
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 2 | 2 | 08-May-14 | 09-May-14 | 96 |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 2 | 2 | 22-May-14 | 23-May-14 | 96 |
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 2 | 2 | 27-May-14 | 28-May-14 | 96 |
| S2-4038 | Stair 2 - Set Mtl Stairs / Railings L17 | 2 | 2 | 29-May-14 | 30-May-14 | 96 |
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - Set Metal Stairs / Railings LL2 | 6 | 6 | 19-Mar-14 | 26-Mar-14 | 132 |
| S3-4002 | Stair 3 - Set Metal Stairs / Railings LL1 | 6 | 6 | 27-Mar-14 | 03-Apr-14 | 132 |
| S3-4004 | Stair 3 - Permanent Railings / Final Finishes | 4 | 4 | 04-Apr-14 | 09-Apr-14 | 132 |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |
| S4-4000 | Stair 4 - Set Metal Stairs / Railings LL2 | 6 | 6 | 03-Mar-14 | 10-Mar-14 | 132 |
| S4-4002 | Stair 4 - Set Metal Stairs / Railings LL1 | 6 | 6 | 11-Mar-14 | 18-Mar-14 | 132 |
| S4-4004 | Stair 4 -Set Metal Stairs / Railings L1 | 6 | 6 | 19-Mar-14 | 26-Mar-14 | 138 |
| S4-4006 | Stair 4 - Permanent Railings / Final Finishes | 4 | 4 | 27-Mar-14 | 01-Apr-14 | 138 |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |
| S6-4000 | Stair 6 - Set Metal Stairs / Railings | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 153 |
| S6-4002 | Stair 6 - Permanent Railings / Final Finishes | 2 | 2 | 10-Mar-14 | 11-Mar-14 | 153 |
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 4 | 07-May-14 | 12-May-14 | 109 |
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 10 | 19-Mar-14 | 01-Apr-14 | 133 |
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes | 5 | 5 | 02-Apr-14 | 08-Apr-14 | 133 |

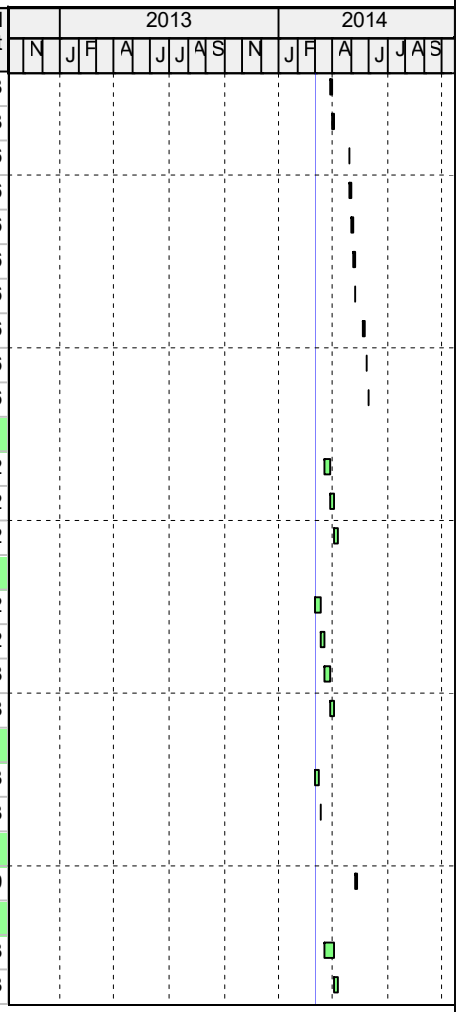



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a -Set Metal Stairs / Railings L1 | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 153 |
| S4a-4002 | Stair 4a - Permanent Railings / Final Finishes | 2 | 2 | 10-Mar-14 | 11-Mar-14 | 153 |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 07-Jun-13 A | | |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 0 | 17-Jun-13 A | 21-Jun-13 A | |
| EL-1004 | Elev - Submittal Approval | 21 | 0 | 21-Jun-13 A | 01-Jan-14 A | |
| EL-1006 | Elev - Release to Manufacturing | 14 | 0 | 02-Jan-14 A | 15-Jan-14 A | |
| EL-1008 | Elev - Fabrication (Engineered Geared) | 95 | 50 | 16-Jan-14 A | 20-Apr-14 | 11 |
| EL-1010 | Elev - Deliver to Jobsite | 1 | 1 | 21-Apr-14 | 21-Apr-14 | 9 |
| EL-1011 | Elev - Elevator Machines Flown & Set At Top Of Hoist | 9 | 9 | 22-Apr-14 | 02-May-14 | 9 |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 5 | 5 | 28-Apr-14 | 02-May-14 | 9 |
| EL-1202 | Elev 1&2 - Mob / Unload & Stage Equip / Materials | 5 | 5 | 28-Apr-14 | 02-May-14 | 9 |
| EL-3402 | Elev 3&4 - Mob / Unload & Stage Equip / Materials | 5 | 5 | 28-Apr-14 | 02-May-14 | 9 |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 5 | 5 | 28-Apr-14 | 02-May-14 | 72 |
| EL-5016 | Elev 5 - Hoistway Walls Complete (GC) | 0 | 0 | | 02-May-14 | 20 |
| EL-1216 | Elev 1&2 - Hoistway Walls Complete (GC) | 0 | 0 | | 02-May-14 | 10 |
| EL-3416 | Elev 3&4 - Hoistway Walls Complete (GC) | 0 | 0 | | 02-May-14 | 9 |
| EL-6016 | Elev 6 - Hoistway Walls Complete (GC) | 0 | 0 | | 02-May-14 | 72 |
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 05-May-14 | | 9 |
| EL-5018 | Elev 5 - Install Machine Room Equipment | 5 | 5 | 05-May-14 | 09-May-14 | 20 |
| EL-1200 | Elev 1&2 - Hoistway Clear & Ready (GC) | 0 | 0 | 05-May-14 | | 9 |
| EL-1218 | Elev 1&2 - Install Machine Room Equipment | 5 | 5 | 05-May-14 | 09-May-14 | 10 |
| EL-3400 | Elev 3&4 - Hoistway Clear & Ready (GC) | 0 | 0 | 05-May-14 | | 9 |
| EL-3418 | Elev 3&4 - Install Machine Room Equipment | 5 | 5 | 05-May-14 | 09-May-14 | 9 |
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 05-May-14 | | 72 |

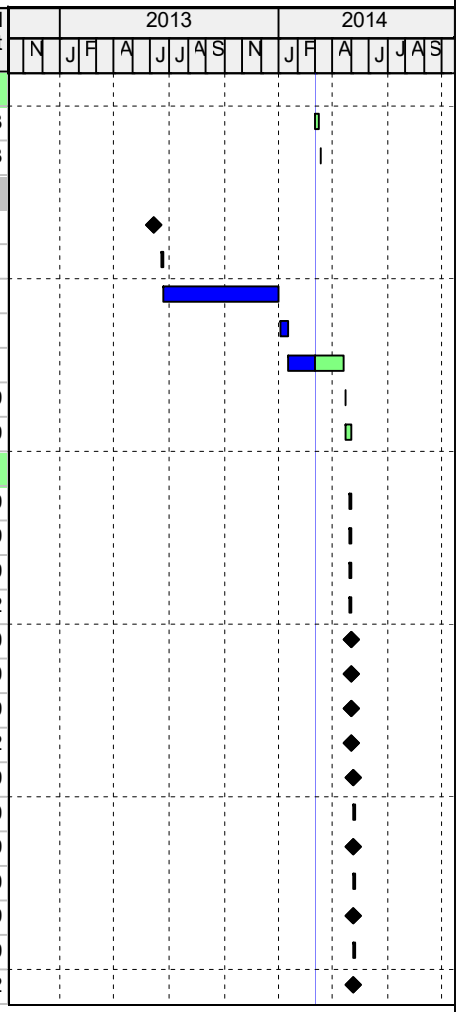



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6018 | Elev 6 - Install Machine Room Equipment | 2 | 2 | 05-May-14 | 06-May-14 | 72 |
| EL-6004 | Elev 6 - Install Cylinders/Rails & Brackets | 4 | 4 | 07-May-14 | 12-May-14 | 72 |
| EL-5004 | Elev 5 - Install Rails & Brackets | 13 | 13 | 12-May-14 | 29-May-14 | 20 |
| EL-1204 | Elev 1&2 - Install Rails & Brackets | 17 | 17 | 12-May-14 | 04-Jun-14 | 10 |
| EL-3404 | Elev 3&4 - Install Rails & Brackets | 18 | 18 | 12-May-14 | 05-Jun-14 | 9 |
| EL-6006 | Elev 6 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 12-May-14 | 72 |
| EL-6007 | Elev 6 - Install Pit Equipment/Car Sling | 3 | 3 | 13-May-14 | 15-May-14 | 72 |
| EL-6010 | Elev 6 - Install Entrances/Doors/Fixtures/Fascia | 3 | 3 | 16-May-14 | 20-May-14 | 72 |
| EL-6012 | Elev 6 - Install Hoistway Equipment/Pipe & Wire | 2 | 2 | 21-May-14 | 22-May-14 | 72 |
| EL-6014 | Elev 6 - Install Cab/Wiring/Door Operator(s) | 5 | 5 | 23-May-14 | 30-May-14 | 72 |
| EL-5006 | Elev 5 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 29-May-14 | 20 |
| EL-5007 | Elev 5 - Install Pit Equipment/Car Sling/CWT Frame/V | 5 | 5 | 30-May-14 | 05-Jun-14 | 20 |
| EL-6022 | Elev 6 - Adjust | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 72 |
| EL-1206 | Elev 1&2 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 04-Jun-14 | 10 |
| EL-1207 | Elev 1&2 - Install Pit Equipment/Car Sling/CWT Fram | 3 | 3 | 05-Jun-14 | 09-Jun-14 | 10 |
| EL-3406 | Elev 3&4 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 05-Jun-14 | 9 |
| EL-5008 | Elev 5 - Install MHoist & Cable | 4 | 4 | 06-Jun-14 | 11-Jun-14 | 20 |
| EL-3407 | Elev 3&4 - Install Pit Equipment/Car Sling/CWT Fram | 5 | 5 | 06-Jun-14 | 12-Jun-14 | 9 |
| EL-6024 | Elev 6 - Clean / Paint / Punchlist | 1 | 1 | 09-Jun-14 | 09-Jun-14 | 72 |
| EL-1208 | Elev 1&2 - Install MHoist & Cable | 5 | 5 | 10-Jun-14 | 16-Jun-14 | 10 |
| EL-6026 | Elev 6 - Inspections | 1 | 1 | 10-Jun-14 | 10-Jun-14 | 103 |
| EL-5010 | Elev 5 - Install Entrances/Doors/Fixtures/Fascia | 21 | 21 | 12-Jun-14 | 11-Jul-14 | 20 |
| EL-3408 | Elev 3&4 - Install Hoist & Cable | 5 | 5 | 13-Jun-14 | 19-Jun-14 | 9 |
| EL-1210 | Elev 1&2 - Install Entrances/Doors/Fixtures/Fascia | 19 | 19 | 17-Jun-14 | 14-Jul-14 | 10 |
| EL-3410 | Elev 3&4 - Install Entrances/Doors/Fixtures/Fascia | 30 | 30 | 20-Jun-14 | 01-Aug-14 | 9 |
| EL-5012 | Elev 5 - Install Hoistway Equipment/Pipe & Wire | 14 | 14 | 14-Jul-14 | 31-Jul-14 | 20 |
| EL-1212 | Elev 1&2 - Install Hoistway Equipment/Pipe & Wire | 17 | 17 | 15-Jul-14 | 06-Aug-14 | 10 |

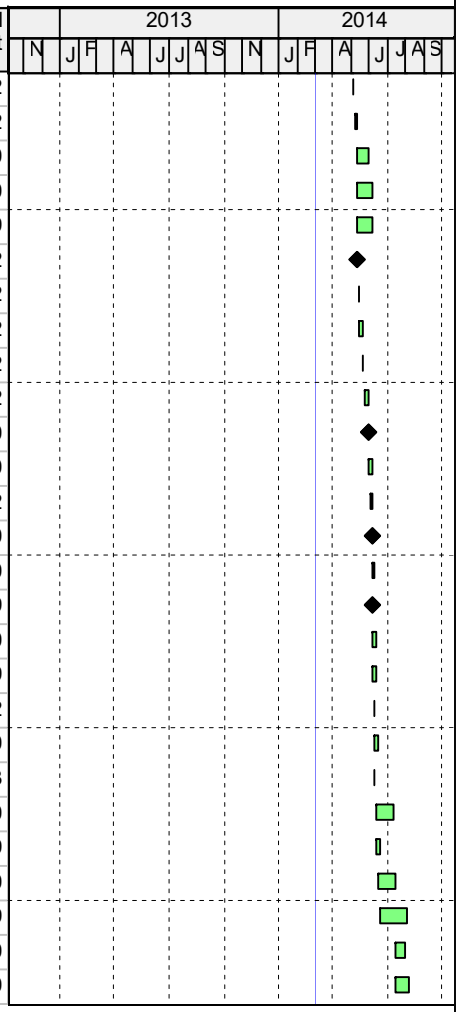


Actual Work | Remaining Work | Critical Remai... | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-5014 | Elev 5 - Install Cab/Wiring/Door Operator(s) | 7 | 7 | 01-Aug-14 | 11-Aug-14 | 20 |
| EL-3412 | Elev 3&4 - Install Hoistway Equipment/Pipe & Wire | 23 | 23 | 04-Aug-14 | 04-Sep-14 | 9 |
| EL-1214 | Elev 1&2 - Install Cab/Wiring/Door Operator(s) | 16 | 16 | 07-Aug-14 | 28-Aug-14 | 10 |
| EL-5022 | Elev 5 - Adjust | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 20 |
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 3 | 3 | 19-Aug-14 | 21-Aug-14 | 20 |
| EL-5026 | Elev 5 - Inspections | 2 | 2 | 22-Aug-14 | 23-Aug-14 | 29 |
| EL-1222 | Elev 1&2 - Adjust | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 10 |
| EL-3414 | Elev 3&4 - Install Cab/Wiring/Door Operator(s) | 10 | 10 | 05-Sep-14 | 18-Sep-14 | 9 |
| EL-1224 | Elev 1&2 - Clean / Paint / Punchlist | 3 | 3 | 08-Sep-14 | 10-Sep-14 | 10 |
| EL-1226 | Elev 1&2 - Inspections | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 14 |
| EL-3422 | Elev 3&4 - Adjust | 5 | 5 | 19-Sep-14 | 25-Sep-14 | 9 |
| EL-3424 | Elev 3&4 - Clean / Paint / Punchlist | 3 | 3 | 26-Sep-14 | 30-Sep-14 | 9 |
| EL-3426 | Elev 3&4 - Inspections | 2 | 2 | 01-Oct-14 | 02-Oct-14 | 13 |
| **Exterior Shell** | | | | | | |
| **Elevations** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2** | | | | | | |
| L3D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Feb-14 A | 12-Feb-14 A | |
| L3-5308 | L3- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 17-Feb-14 A | 21-Feb-14 A | |
| L4D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Feb-14 A | 19-Feb-14 A | |
| L4-5308 | L4- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Feb-14 A | 28-Feb-14 A | |
| L5D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Feb-14 A | 26-Feb-14 A | |
| L5-5308 | L5- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 15 |
| L6D5308 | Deliver/Stock Wall Panels | 1 | 1 | 05-Mar-14 | 05-Mar-14 | 17 |
| LL2-5308 | LL2 Thru L4 - Support Frame/Sheathing for Metal Wa | 10 | 10 | 10-Mar-14 | 21-Mar-14 | 8 |
| L6-5308 | L6- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 10-Mar-14 | 14-Mar-14 | 15 |
| L7D5308 | Deliver/Stock Wall Panels | 1 | 1 | 12-Mar-14 | 12-Mar-14 | 17 |

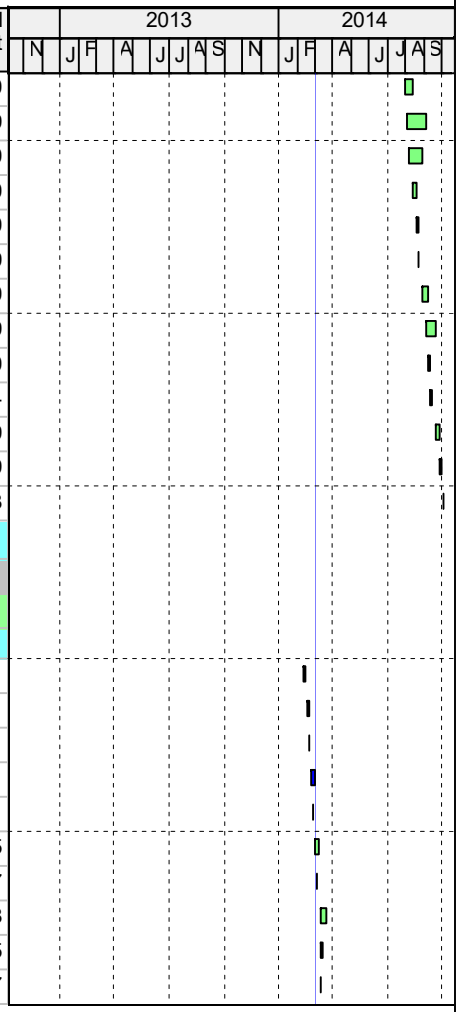



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L7-5308 | L7- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 17-Mar-14 | 21-Mar-14 | 15 |
| L8D5308 | Deliver/Stock Wall Panels | 1 | 1 | 19-Mar-14 | 19-Mar-14 | 17 |
| LL1-5308 | LL1 - Support Frame/Sheathing for Metal Wall Panel | 10 | 10 | 24-Mar-14 | 04-Apr-14 | 8 |
| L8-5308 | L8- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 24-Mar-14 | 28-Mar-14 | 15 |
| L9D5308 | Deliver/Stock Wall Panels | 1 | 1 | 26-Mar-14 | 26-Mar-14 | 17 |
| L9-5308 | L9- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 31-Mar-14 | 04-Apr-14 | 15 |
| 10D5308 | Deliver/Stock Wall Panels | 1 | 1 | 02-Apr-14 | 02-Apr-14 | 17 |
| L1-5308 | L1 - Support Frame/Sheathing for Metal Wall Panels | 9 | 9 | 07-Apr-14 | 17-Apr-14 | 8 |
| L10-5308 | L10- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 07-Apr-14 | 11-Apr-14 | 15 |
| 11D5308 | Deliver/Stock Wall Panels | 1 | 1 | 09-Apr-14 | 09-Apr-14 | 17 |
| LL2-5116 | LL2 Thru L4 - Metal Wall Panels (East/North) | 10 | 10 | 14-Apr-14 | 25-Apr-14 | 25 |
| L11-5308 | L11- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 14-Apr-14 | 18-Apr-14 | 15 |
| 12D5308 | Deliver/Stock Wall Panels | 1 | 1 | 23-Apr-14 | 23-Apr-14 | 21 |
| L12-5308 | L12- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 28-Apr-14 | 02-May-14 | 21 |
| 14D5308 | Deliver/Stock Wall Panels | 1 | 1 | 30-Apr-14 | 30-Apr-14 | 23 |
| L14-5308 | L14 - Support Frame/Sheathing for Metal Wall Panel | 5 | 5 | 05-May-14 | 09-May-14 | 21 |
| 15D5308 | Deliver/Stock Wall Panels | 1 | 1 | 07-May-14 | 07-May-14 | 23 |
| L15-5308 | L15 - Support Frame/Sheathing for Metal Wall Panel | 5 | 5 | 12-May-14 | 16-May-14 | 21 |
| 16D5308 | Deliver/Stock Wall Panels | 1 | 1 | 14-May-14 | 14-May-14 | 23 |
| L16-5308 | L16- Support Frame/Sheathing for Metal Wall Panels | 5 | 5 | 19-May-14 | 23-May-14 | 21 |
| 17D5308 | Deliver/Stock Wall Panels | 1 | 1 | 21-May-14 | 21-May-14 | 102 |
| L17-5308 | L17 - Support Frame/Sheathing for Metal Wall Panel | 5 | 5 | 27-May-14 | 31-May-14 | 25 |
| **Lower Level 1** | | | | | | |
| LL1-5116 | LL1 - Metal Wall Panels (East/North) | 10 | 10 | 28-Apr-14 | 09-May-14 | 25 |
| **Level 1** | | | | | | |
| L1-5116 | L1 - Metal Wall Panels | 10 | 10 | 12-May-14 | 23-May-14 | 25 |
| L1-5102 | L1 - Storefront Frames | 10 | 10 | 27-May-14 | 09-Jun-14 | 85 |

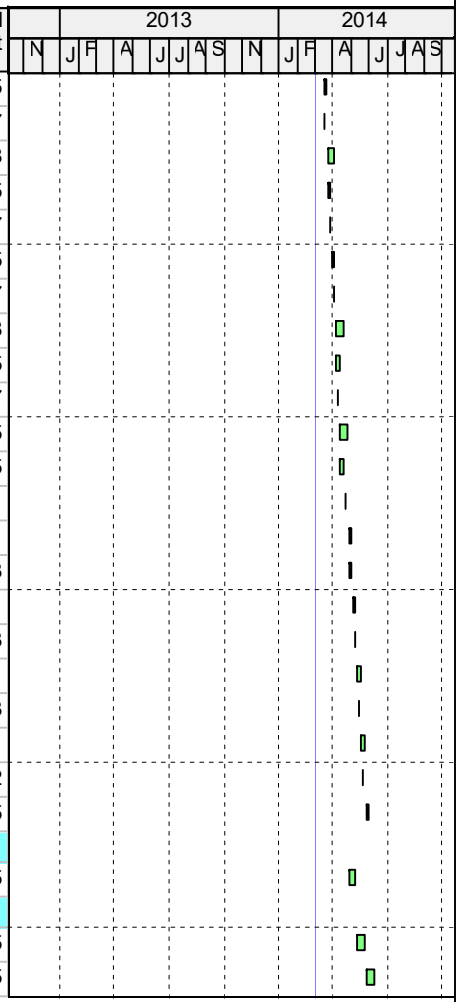



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L3-5116 | L3 - Metal Wall Panels | 10 | 10 | 02-Jun-14 | 13-Jun-14 | 21 |
| L1-5104 | L1 - Storefront Glazing | 5 | 5 | 10-Jun-14 | 16-Jun-14 | 85 |
| EP-5110 | L1 - Revolving Doors | 5 | 5 | 10-Jun-14 | 16-Jun-14 | 85 |
| L3-5102 | L3- Storefront Frames | 10 | 10 | 16-Jun-14 | 27-Jun-14 | 71 |
| L4-5116 | L4 - Metal Wall Panels | 5 | 5 | 16-Jun-14 | 20-Jun-14 | 21 |
| L5-5116 | L5 - Metal Wall Panels | 5 | 5 | 23-Jun-14 | 27-Jun-14 | 21 |
| L3-5104 | L3 - Storefront Glazing | 5 | 5 | 30-Jun-14 | 07-Jul-14 | 71 |
| L6-5116 | L6 - Metal Wall Panels | 5 | 5 | 30-Jun-14 | 07-Jul-14 | 21 |
| L7-5116 | L7 - Metal Wall Panels | 5 | 5 | 08-Jul-14 | 14-Jul-14 | 21 |
| L8-5116 | L8 - Metal Wall Panels | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 21 |
| L9-5116 | L9 - Metal Wall Panels | 5 | 5 | 22-Jul-14 | 28-Jul-14 | 21 |
| L10-5116 | L10 - Metal Wall Panels | 5 | 5 | 29-Jul-14 | 04-Aug-14 | 21 |
| L11-5116 | L11 - Metal Wall Panels | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 21 |
| L12-5116 | L12 - Metal Wall Panels | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 21 |
| L14-5116 | L14 - Metal Wall Panels | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 21 |
| L15-5116 | L15 - Metal Wall Panels | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 21 |
| L16-5116 | L16 - Metal Wall Panels | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 21 |
| L17-5116 | L17 - Metal Wall Panels | 5 | 5 | 10-Sep-14 | 16-Sep-14 | 21 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Levels 3-4** | | | | | | |
| L3-5130 | L3 - Install Punch Windows | 5 | 5 | 24-Feb-14 A | 07-Mar-14 | 80 |
| L4-5130 | L4 - Install Punch Windows | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 90 |
| L5-5130 | L5 - Install Punch Windows | 5 | 5 | 10-Mar-14 | 14-Mar-14 | 90 |
| L6-5130 | L6- Install Punch Windows | 5 | 5 | 17-Mar-14 | 21-Mar-14 | 90 |
| L7-5130 | L7 - Install Punch Windows | 5 | 5 | 24-Mar-14 | 28-Mar-14 | 90 |
| L8-5130 | L8 - Install Punch Windows | 5 | 5 | 31-Mar-14 | 04-Apr-14 | 90 |
| L9-5130 | L9 - Install Punch Windows | 5 | 5 | 07-Apr-14 | 11-Apr-14 | 90 |

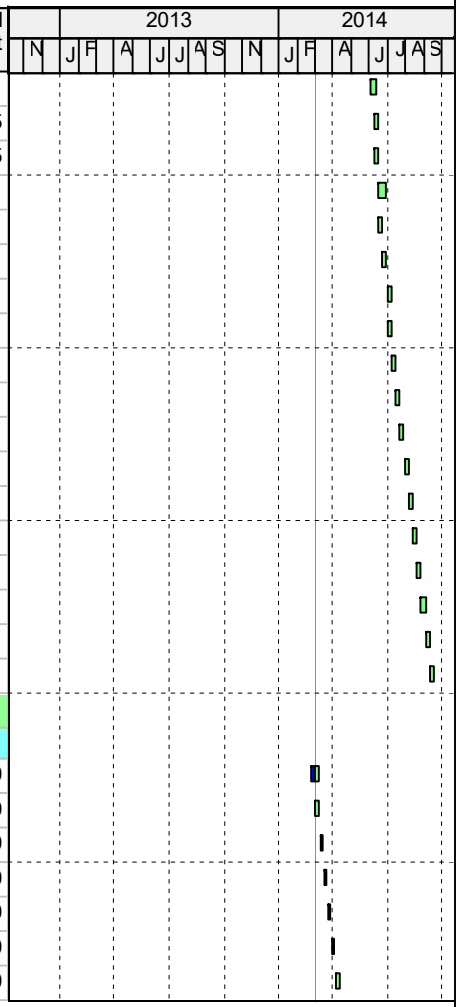



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-5130 | L10 - Install Punch Windows | 5 | 5 | 14-Apr-14 | 18-Apr-14 | 90 |
| L11-5130 | L11 - Install Punch Windows | 5 | 5 | 21-Apr-14 | 25-Apr-14 | 90 |
| L12-5130 | L12 - Install Punch Windows | 5 | 5 | 05-May-14 | 09-May-14 | 85 |
| L14-5130 | L14 - Install Punch Windows | 5 | 5 | 12-May-14 | 16-May-14 | 85 |
| L15-5130 | L15 - Install Punch Windows | 5 | 5 | 19-May-14 | 23-May-14 | 85 |
| L16-5130 | L16 - Install Punch Windows | 5 | 5 | 27-May-14 | 02-Jun-14 | 85 |
| L17-5130 | L17 - Install Punch Windows | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 86 |
| Roofs | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 5 | 08-May-14 | 14-May-14 | 102 |
| RF-4026 | L1 - City Park - Protection Board | 3 | 3 | 15-May-14 | 19-May-14 | 102 |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 2 | 20-May-14 | 21-May-14 | 102 |
| **Pool Membrane - (elev 18')** | | | | | | |
| RF-4034 | Pool Waterproofing / Membrane | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 21 |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 15 | 15 | 02-May-14 | 22-May-14 | 8 |
| RF-4010 | AR - Set Mechanical Equipment | 5 | 5 | 23-May-14 | 30-May-14 | 96 |
| RF-4012 | AR - Coping / Flashing | 4 | 4 | 23-May-14 | 29-May-14 | 97 |
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 5 | 5 | 23-May-14 | 30-May-14 | 9 |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |
| PC-4008 | RF - Entry / Porte Cochere Roofing System | 15 | 15 | 02-May-14 | 22-May-14 | 9 |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | Rf - Upper Ballroom Roofing System | 10 | 10 | 18-Apr-14 | 01-May-14 | 8 |
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 10 | 10 | 30-Jun-14 | 14-Jul-14 | 41 |
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |

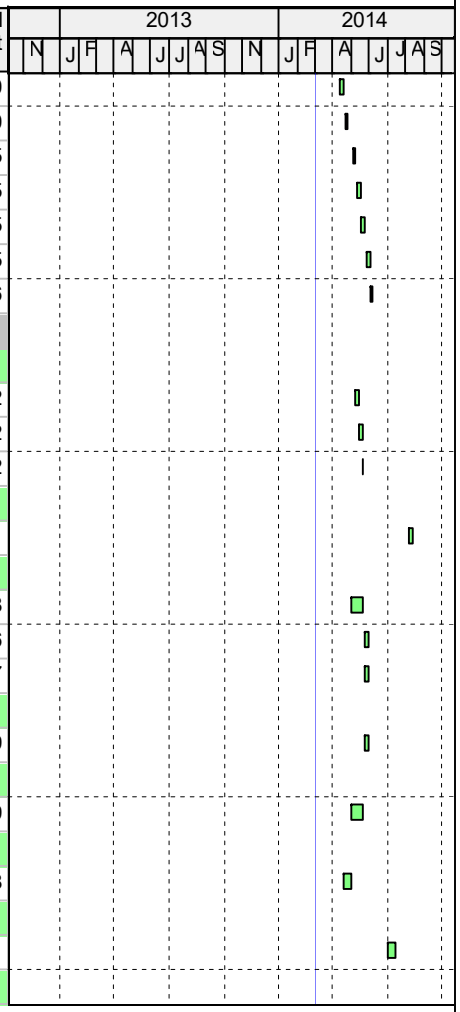



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| RF-4018 | TR - Terrace Roof - Roofing System | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 31 |
| RF-4020 | TR - Terrace Roof - Coping / Flashing | 3 | 3 | 26-Aug-14 | 28-Aug-14 | 33 |
| RF-4022 | TR - Terrace Roof - Glass Railing | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 31 |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Substrates / Land Mech | 20 | 20 | 22-May-14 | 19-Jun-14 | 73 |
| RF-4002 | Tower Roof - Roofing / Roof Structures | 18 | 18 | 06-Jun-14 | 01-Jul-14 | 73 |
| **PH - Roof - (elev 173')** | | | | | | |
| RF-4030 | PH - Roofing System | 5 | 5 | 05-May-14 | 09-May-14 | 9 |
| RF-4032 | PH - Coping / Flashing | 2 | 2 | 12-May-14 | 13-May-14 | 108 |
| **Rough-In's** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6002 | LL4 - Layout | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| LL4-6008 | LL4 - Int Wall Framing | 5 | 5 | 09-Dec-13 A | 07-Mar-14 | 46 |
| LL4-6012 | LL4 - Fire Sprinkler Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6014 | LL4 - Plumbing Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6018 | LL4 - HVAC Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6004 | LL4 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL4-6010 | LL4 - F/P Curbs | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 56 |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 2 | 03-Mar-14 | 04-Mar-14 | 59 |
| LL4-6016 | LL4 - Electrical Rl | 10 | 10 | 10-Mar-14 | 21-Mar-14 | 46 |
| LL4-6020 | LL4 - H Mtl Frames | 3 | 3 | 10-Mar-14 | 12-Mar-14 | 53 |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties Rl | 8 | 8 | 10-Mar-14 | 19-Mar-14 | 147 |
| LL4-6024 | LL4 - Inspections | 2 | 2 | 24-Mar-14 | 25-Mar-14 | 46 |
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6002 | LL3 - Layout | 1 | 0 | 19-Nov-13 A | 19-Nov-13 A | |
| LL3-6008 | LL3 - Int Wall Framing | 5 | 5 | 09-Dec-13 A | 07-Mar-14 | 51 |

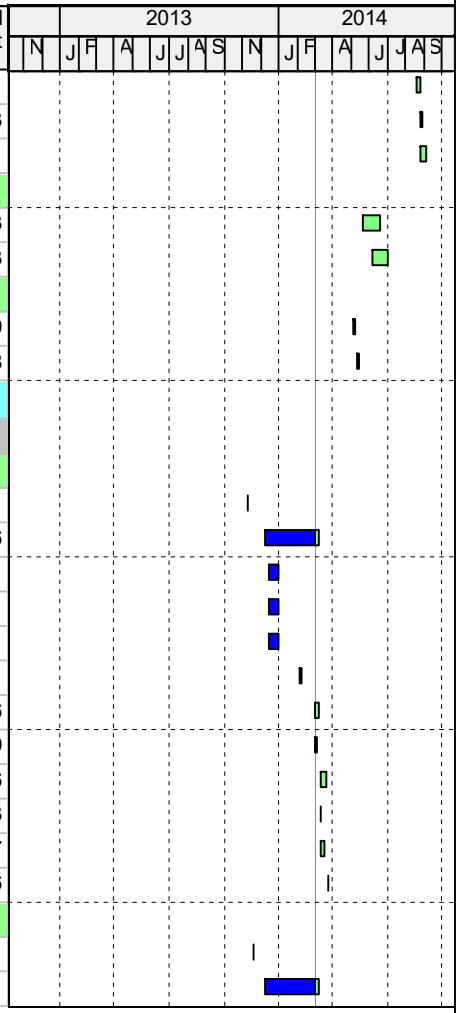



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-6012 | LL3 - Fire Sprinkler RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6014 | LL3 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6018 | LL3 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6004 | LL3 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL3-6010 | LL3 - F/P Curbs | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 61 |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 2 | 03-Mar-14 | 04-Mar-14 | 64 |
| LL3-6016 | LL3 - Electrical RI | 10 | 10 | 10-Mar-14 | 21-Mar-14 | 51 |
| LL3-6020 | LL3 - H Mtl Frames | 3 | 3 | 10-Mar-14 | 12-Mar-14 | 58 |
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties RI | 8 | 8 | 10-Mar-14 | 19-Mar-14 | 147 |
| LL3-6024 | LL3 - Inspections | 2 | 2 | 24-Mar-14 | 25-Mar-14 | 51 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6002 | LL2 - Layout | 1 | 0 | 14-Jan-14 A | 14-Jan-14 A | |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| LL2-6012 | LL2 - Fire Sprinkler RI | 10 | 0 | 21-Jan-14 A | 03-Feb-14 A | |
| LL2-6014 | LL2 - Plumbing RI | 10 | 0 | 21-Jan-14 A | 14-Feb-14 A | |
| LL2-6016 | LL2 - Electrical RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2-6018 | LL2 - HVAC RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2–6004 | LL2 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL2-6020 | LL2 - H Mtl Frames | 3 | 3 | 03-Mar-14 | 05-Mar-14 | 68 |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties RI | 8 | 8 | 03-Mar-14 | 12-Mar-14 | 152 |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 4 | 03-Mar-14 | 06-Mar-14 | 67 |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 3 | 03-Mar-14 | 05-Mar-14 | 8 |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 2 | 2 | 06-Mar-14 | 07-Mar-14 | 8 |
| LL2-6024 | LL2 - Inspections | 2 | 2 | 07-Mar-14 | 10-Mar-14 | 67 |
| LL2E-6004 | LL2 - CMU Walls | 10 | 10 | 18-Mar-14 | 31-Mar-14 | 114 |
| LL2E-6020 | LL2 - H Mtl Frames | 3 | 3 | 18-Mar-14 | 20-Mar-14 | 146 |
| LL2E-6008 | LL2 - Int Wall Framing | 5 | 5 | 01-Apr-14 | 07-Apr-14 | 114 |

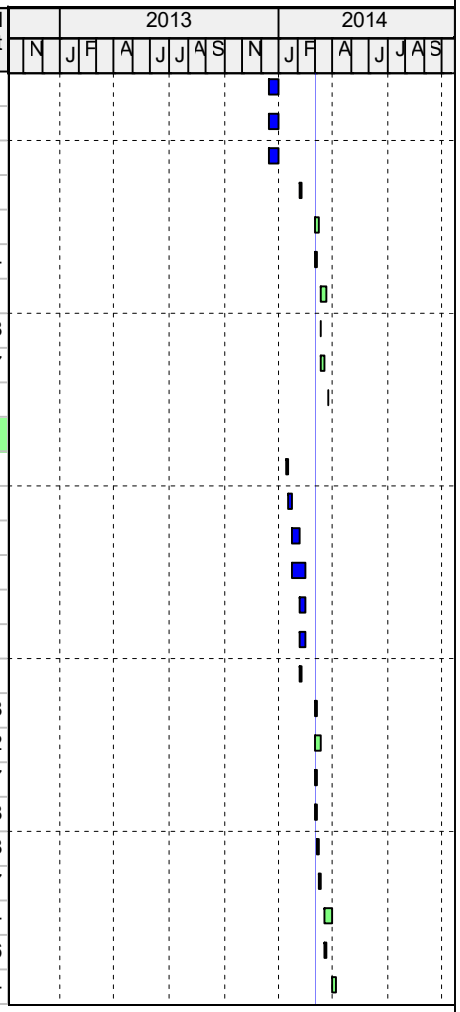



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-6015 | LL2 - Main Elect Room Set Equip / RI - Power to Ma | 20 | 20 | 08-Apr-14 | 05-May-14 | 114 |
| LL2E-6012 | LL2 - Fire Sprinkler RI | 8 | 8 | 08-Apr-14 | 17-Apr-14 | 126 |
| LL2E-6014 | LL2 - Plumbing RI | 8 | 8 | 08-Apr-14 | 17-Apr-14 | 126 |
| LL2E-6016 | LL2 - Electrical RI | 8 | 8 | 08-Apr-14 | 17-Apr-14 | 126 |
| LL2E-6018 | LL2 - HVAC RI | 8 | 8 | 08-Apr-14 | 17-Apr-14 | 126 |
| LL2E-6022 | LL2 - Fire Alarm / Elec Specialties RI | 8 | 8 | 08-Apr-14 | 17-Apr-14 | 126 |
| LL2-6010 | LL2 - F/P Curbs @ Parking | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 56 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6002 | Layout | 3 | 0 | 03-Jan-14 A | 08-Jan-14 A | |
| LL1-6008 | Int Wall Framing & Inspection | 6 | 0 | 08-Jan-14 A | 03-Mar-14 | 31 |
| LL1-Z2-6002 | Layout | 3 | 0 | 08-Jan-14 A | 14-Jan-14 A | |
| LL1-Z3-6002 | Layout | 3 | 0 | 14-Jan-14 A | 17-Jan-14 A | |
| LL1-Z2-6008 | Int Wall Framing & Inspection | 6 | 0 | 17-Jan-14 A | 03-Mar-14 | 56 |
| LL1-Z3-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-Jan-14 A | 04-Feb-14 A | |
| LL1-6004 | CMU Walls | 3 | 14 | 03-Feb-14 A | 20-Mar-14 | 20 |
| LL1-Z2-6004 | CMU Walls | 3 | 14 | 03-Feb-14 A | 20-Mar-14 | 45 |
| LL1-Z3-6004 | CMU Walls | 3 | 14 | 03-Feb-14 A | 20-Mar-14 | 37 |
| LL1-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 25-Mar-14 | 40 |
| LL1-6014 | Plumbing RI | 20 | 20 | 17-Feb-14 A | 21-Apr-14 | 20 |
| LL1-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 25-Mar-14 | 40 |
| LL1-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 25-Mar-14 | 40 |
| LL1-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 25-Mar-14 | 40 |
| LL1-Z2-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 25-Mar-14 | 45 |
| LL1-Z2-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 25-Mar-14 | 45 |
| LL1-Z2-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 25-Mar-14 | 45 |
| LL1-Z2-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 25-Mar-14 | 45 |

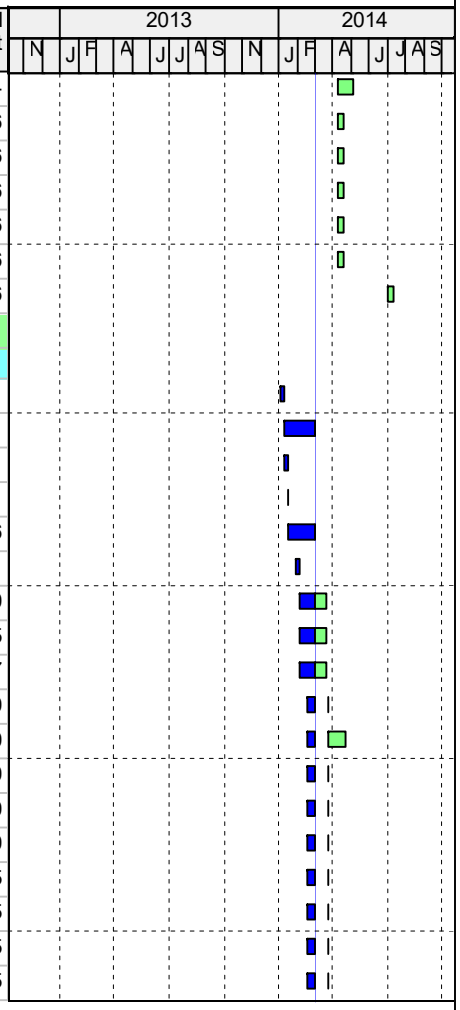


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 25-Mar-14 | 45 |
| LL1-Z3-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 25-Mar-14 | 50 |
| LL1-Z3-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 25-Mar-14 | 50 |
| LL1-Z3-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 25-Mar-14 | 50 |
| LL1-Z3-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 25-Mar-14 | 50 |
| LL1-Z3-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 25-Mar-14 | 50 |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 3 | 06-Mar-14 | 10-Mar-14 | 22 |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 3 | 3 | 11-Mar-14 | 13-Mar-14 | 151 |
| LL1-6010 | CMU Seismic Clips | 2 | 2 | 21-Mar-14 | 24-Mar-14 | 20 |
| LL1-Z2-6010 | CMU Seismic Clips | 2 | 2 | 21-Mar-14 | 24-Mar-14 | 45 |
| LL1-Z3-6010 | CMU Seismic Clips | 2 | 2 | 21-Mar-14 | 24-Mar-14 | 50 |
| L1B-6004 | CMU Walls | 3 | 3 | 21-Mar-14 | 25-Mar-14 | 37 |
| L1L-6004 | CMU Walls | 3 | 3 | 21-Mar-14 | 25-Mar-14 | 37 |
| L1K-6004 | CMU Walls | 3 | 3 | 21-Mar-14 | 25-Mar-14 | 37 |
| LL1-Z2-6009 | Frame Ceilings | 10 | 10 | 25-Mar-14 | 07-Apr-14 | 45 |
| LL1-Z3-6009 | Frame Ceilings | 10 | 10 | 25-Mar-14 | 07-Apr-14 | 50 |
| L1B-6010 | CMU Seismic Clips | 2 | 2 | 26-Mar-14 | 27-Mar-14 | 37 |
| L1L-6010 | CMU Seismic Clips | 2 | 2 | 26-Mar-14 | 27-Mar-14 | 37 |
| L1K-6010 | CMU Seismic Clips | 2 | 2 | 26-Mar-14 | 27-Mar-14 | 37 |
| LL1-Z2-6020 | Hollow Metal Door Frames | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 45 |
| LL1-Z2C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 45 |
| LL1-Z2C-6014 | Complete Plumbing RI @ Ceilings | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 45 |
| LL1-Z2C-6016 | Complete Electrical RI @ Ceilings | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 45 |
| LL1-Z2C-6018 | Complete HVAC RI @ Ceilings | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 45 |
| LL1-Z2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 45 |
| LL1-Z3-6020 | Hollow Metal Door Frames | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 50 |
| LL1-Z3C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 50 |

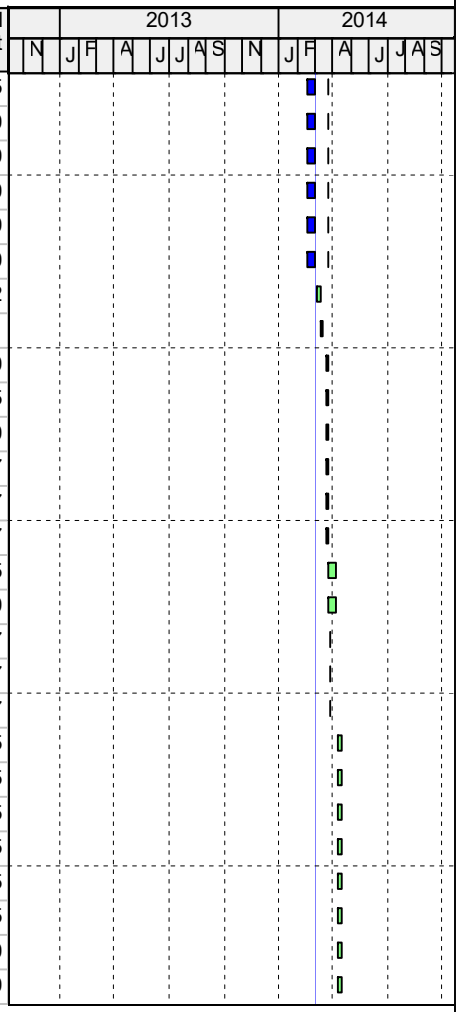



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3C-6014 | Complete Plumbing RI @ Ceilings | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 50 |
| LL1-Z3C-6016 | Complete Electrical RI @ Ceilings | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 50 |
| LL1-Z3C-6018 | Complete HVAC RI @ Ceilings | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 50 |
| LL1-Z3C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 5 | 08-Apr-14 | 14-Apr-14 | 50 |
| L1B-6002 | Layout | 3 | 3 | 14-Apr-14 | 16-Apr-14 | 9 |
| LL1-Z2-6024 | Inspections for Cover | 2 | 2 | 15-Apr-14 | 16-Apr-14 | 45 |
| LL1-Z3-6024 | Inspections for Cover | 2 | 2 | 15-Apr-14 | 16-Apr-14 | 50 |
| L1B-6008 | Int Wall Framing & Inspection | 6 | 6 | 17-Apr-14 | 24-Apr-14 | 12 |
| L1L-6002 | Layout | 3 | 3 | 17-Apr-14 | 21-Apr-14 | 9 |
| LL1-6009 | Frame Ceilings | 10 | 10 | 22-Apr-14 | 05-May-14 | 20 |
| L1L-6008 | Int Wall Framing & Inspection | 6 | 6 | 22-Apr-14 | 29-Apr-14 | 9 |
| L1K-6002 | Layout | 3 | 3 | 22-Apr-14 | 24-Apr-14 | 11 |
| L1K-6008 | Int Wall Framing & Inspection | 4 | 4 | 25-Apr-14 | 30-Apr-14 | 11 |
| L1B-6012 | Fire Sprinkler RI | 10 | 10 | 02-May-14 | 15-May-14 | 12 |
| L1B-6014 | Plumbing RI | 10 | 10 | 02-May-14 | 15-May-14 | 12 |
| L1B-6016 | Electrical RI | 10 | 10 | 02-May-14 | 15-May-14 | 12 |
| L1B-6018 | HVAC RI | 10 | 10 | 02-May-14 | 15-May-14 | 12 |
| L1B-6022 | Fire Alarm / Elec Specialties RI | 10 | 10 | 02-May-14 | 15-May-14 | 12 |
| L1K-6012 | Fire Sprinkler RI | 10 | 10 | 05-May-14 | 16-May-14 | 11 |
| L1K-6014 | Plumbing RI | 10 | 10 | 05-May-14 | 16-May-14 | 11 |
| L1K-6016 | Electrical RI | 10 | 10 | 05-May-14 | 16-May-14 | 11 |
| L1K-6018 | HVAC RI | 10 | 10 | 05-May-14 | 16-May-14 | 11 |
| L1K-6022 | Fire Alarm / Elec Specialties RI | 10 | 10 | 05-May-14 | 16-May-14 | 11 |
| LL1-6020 | Hollow Metal Door Frames | 5 | 5 | 06-May-14 | 12-May-14 | 20 |
| LL1C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 5 | 06-May-14 | 12-May-14 | 20 |
| LL1C-6014 | Complete Plumbing RI @ Ceilings | 5 | 5 | 06-May-14 | 12-May-14 | 20 |
| LL1C-6016 | Complete Electrical RI @ Ceilings | 5 | 5 | 06-May-14 | 12-May-14 | 20 |





© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1C-6018 | Complete HVAC RI @ Ceilings | 5 | 5 | 06-May-14 | 12-May-14 | 20 |
| LL1C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 5 | 06-May-14 | 12-May-14 | 20 |
| L1L-6012 | Fire Sprinkler RI | 10 | 10 | 07-May-14 | 20-May-14 | 9 |
| L1L-6014 | Plumbing RI | 10 | 10 | 07-May-14 | 20-May-14 | 9 |
| L1L-6016 | Electrical RI | 10 | 10 | 07-May-14 | 20-May-14 | 9 |
| L1L-6018 | HVAC RI | 10 | 10 | 07-May-14 | 20-May-14 | 9 |
| L1L-6022 | Fire Alarm / Elec Specialties RI | 10 | 10 | 07-May-14 | 20-May-14 | 9 |
| LL1-6024 | Inspections for Cover | 2 | 2 | 13-May-14 | 14-May-14 | 20 |
| L1B-6009 | Frame Ceilings | 10 | 10 | 16-May-14 | 30-May-14 | 12 |
| L1K-6009 | Frame Ceilings | 10 | 10 | 19-May-14 | 02-Jun-14 | 11 |
| L1L-6009 | Frame Ceilings | 10 | 10 | 21-May-14 | 04-Jun-14 | 9 |
| L1B-6020 | Hollow Metal Door Frames | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 12 |
| L1BC-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 12 |
| L1BC-6014 | Complete Plumbing RI @ Ceilings | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 12 |
| L1BC-6016 | Complete Electrical RI @ Ceilings | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 12 |
| L1BC-6018 | Complete HVAC RI @ Ceilings | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 12 |
| L1BC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 12 |
| L1K-6020 | Hollow Metal Door Frames | 5 | 5 | 03-Jun-14 | 09-Jun-14 | 11 |
| L1KC-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 5 | 03-Jun-14 | 09-Jun-14 | 11 |
| L1KC-6014 | Complete Plumbing RI @ Ceilings | 5 | 5 | 03-Jun-14 | 09-Jun-14 | 11 |
| L1KC-6016 | Complete Electrical RI @ Ceilings | 5 | 5 | 03-Jun-14 | 09-Jun-14 | 11 |
| L1KC-6018 | Complete HVAC RI @ Ceilings | 5 | 5 | 03-Jun-14 | 09-Jun-14 | 11 |
| L1KC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 5 | 03-Jun-14 | 09-Jun-14 | 11 |
| L1L-6020 | Hollow Metal Door Frames | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 9 |
| L1LC-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 9 |
| L1LC-6014 | Complete Plumbing RI @ Ceilings | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 9 |
| L1LC-6016 | Complete Electrical RI @ Ceilings | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 9 |

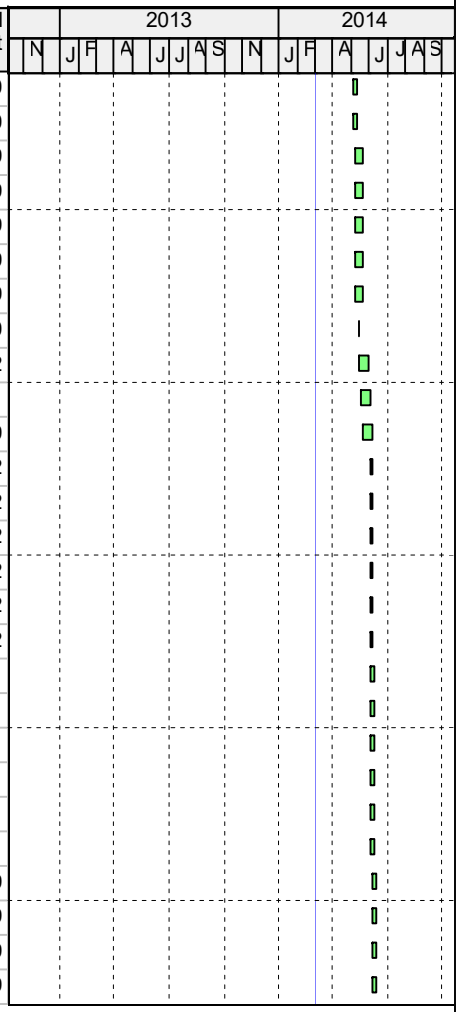



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1LC-6018 | Complete HVAC RI @ Ceilings | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 9 |
| L1LC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 9 |
| L1B-6024 | Inspections for Cover | 2 | 2 | 09-Jun-14 | 10-Jun-14 | 12 |
| L1K-6024 | Inspections for Cover | 2 | 2 | 10-Jun-14 | 11-Jun-14 | 11 |
| L1L-6024 | Inspections for Cover | 2 | 2 | 12-Jun-14 | 13-Jun-14 | 9 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 5 | 11-Mar-14 | 17-Mar-14 | 22 |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6002 | L2 - Layout | 1 | 1 | 03-Mar-14 | 03-Mar-14 | 36 |
| L02-6004 | L2 - CMU Walls | 5 | 5 | 04-Mar-14 | 10-Mar-14 | 46 |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 1 | 11-Mar-14 | 11-Mar-14 | 65 |
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 5 | 11-Mar-14 | 17-Mar-14 | 31 |
| L02-6006 | L2 - Support Frame/Sheathing for Metal Panels | 10 | 10 | 18-Apr-14 | 01-May-14 | 8 |
| L02-6008 | L2 - Int Wall Framing | 10 | 10 | 02-May-14 | 15-May-14 | 8 |
| L02-6012 | L2 - Fire Sprinkler RI | 10 | 10 | 16-May-14 | 30-May-14 | 8 |
| L02-6014 | L2 - Plumbing RI | 10 | 10 | 16-May-14 | 30-May-14 | 8 |
| L02-6016 | L2 - Electrical RI | 10 | 10 | 16-May-14 | 30-May-14 | 8 |
| L02-6018 | L2 - HVAC RI | 10 | 10 | 16-May-14 | 30-May-14 | 8 |
| L02-6020 | L2 - H Mtl Frames | 5 | 5 | 16-May-14 | 22-May-14 | 101 |
| L02-6022 | L2 - Fire Alarm / Elec Specialties RI | 10 | 10 | 16-May-14 | 30-May-14 | 96 |
| L02-6024 | L2 - Inspections | 2 | 2 | 02-Jun-14 | 03-Jun-14 | 8 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L03-8219 | HVAC Risers | 5 | 9 | 11-Feb-14 A | 13-Mar-14 | 2 |
| L03-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 11-Feb-14 A | 07-Mar-14 | 0 |
| L03-6002 | Layout | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| L04-8219 | HVAC Risers | 5 | 9 | 13-Feb-14 A | 13-Mar-14 | 7 |

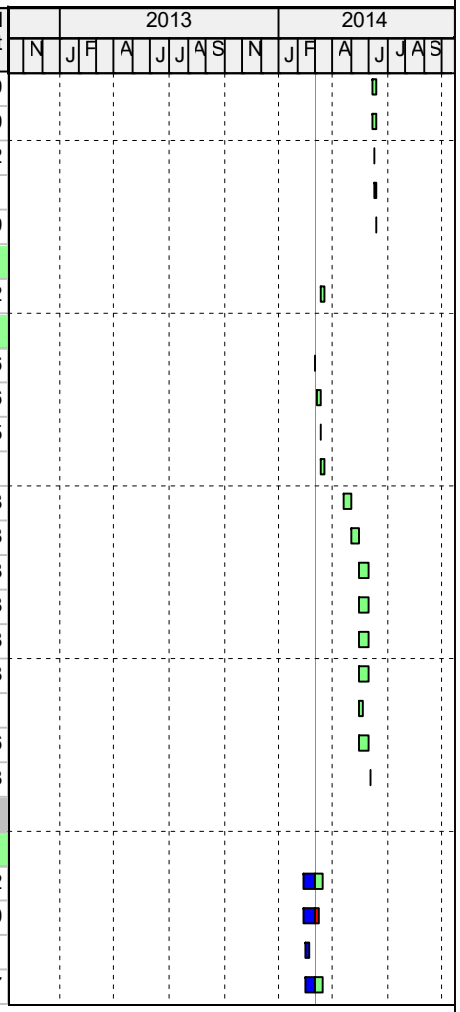



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| L05-8219 | HVAC Risers | 5 | 5 | 17-Feb-14 A | 07-Mar-14 | 14 |
| L05-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 17-Feb-14 A | 21-Feb-14 A | |
| L03-6008 | Frame Shaft Walls | 3 | 6 | 18-Feb-14 A | 17-Mar-14 | 0 |
| L04-6002 | Layout | 5 | 0 | 19-Feb-14 A | 25-Feb-14 A | |
| L04-6008 | Frame Shaft Walls | 3 | 11 | 20-Feb-14 A | 17-Mar-14 | 5 |
| L03-6011 | PreRock Shafts | 2 | 2 | 24-Feb-14 A | 20-Mar-14 | 2 |
| L03-6010 | Frame Walls | 5 | 1 | 25-Feb-14 A | 03-Mar-14 | 15 |
| L05-6002 | Layout | 5 | 3 | 27-Feb-14 A | 05-Mar-14 | 21 |
| L03-6012 | Fire Sprinkler Mains | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 15 |
| L03-6004 | CMU Wall/Clips | 3 | 3 | 03-Mar-14 | 05-Mar-14 | 157 |
| L03-6014 | Set Tubs & Plumbing RI | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 15 |
| L03-6016 | Electrical RI | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 15 |
| L03-6018 | HVAC RI | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 15 |
| L03-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 15 |
| L03-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Mar-14 | | 10 |
| L04-6004 | CMU Wall/Clips | 3 | 3 | 03-Mar-14 | 05-Mar-14 | 157 |
| L04-6010 | Frame Walls | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 16 |
| L04-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Mar-14 | | 15 |
| L06-8219 | HVAC Risers | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 19 |
| L06-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 16 |
| L07-8219 | HVAC Risers | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 155 |
| L07-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 20 |
| L08-8219 | HVAC Risers | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 155 |
| L08-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 24 |
| L09-8219 | HVAC Risers | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 155 |
| L09-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 03-Mar-14 | 07-Mar-14 | 29 |

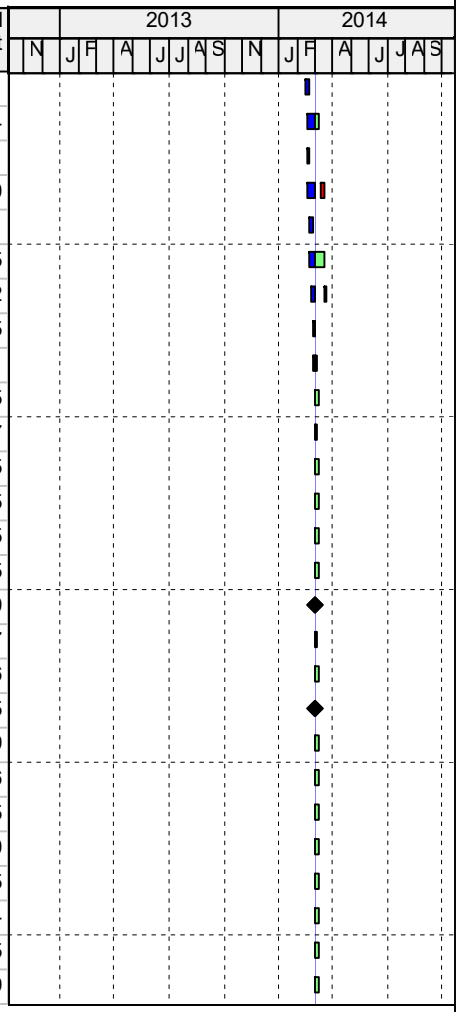



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6020 | Install Hollow Metal Frames | 3 | 3 | 04-Mar-14 | 06-Mar-14 | 19 |
| L05-6008 | Frame Shaft Walls | 3 | 3 | 05-Mar-14 | 07-Mar-14 | 14 |
| L05-6004 | CMU Wall/Clips | 3 | 3 | 06-Mar-14 | 10-Mar-14 | 154 |
| L06-6002 | Layout | 5 | 5 | 06-Mar-14 | 12-Mar-14 | 21 |
| L10-8219 | HVAC Risers | 5 | 5 | 06-Mar-14 | 12-Mar-14 | 152 |
| L10-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 06-Mar-14 | 12-Mar-14 | 31 |
| L04-6012 | Fire Sprinkler Mains | 5 | 5 | 07-Mar-14 | 13-Mar-14 | 16 |
| L04-6014 | Set Tubs & Plumbing RI | 5 | 5 | 07-Mar-14 | 13-Mar-14 | 16 |
| L04-6016 | Electrical RI | 5 | 5 | 07-Mar-14 | 13-Mar-14 | 16 |
| L04-6018 | HVAC RI | 5 | 5 | 07-Mar-14 | 13-Mar-14 | 16 |
| L04-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 07-Mar-14 | 13-Mar-14 | 16 |
| L04-6020 | Install Hollow Metal Frames | 3 | 3 | 10-Mar-14 | 12-Mar-14 | 20 |
| L05-6009 | Inspect Shafts | 1 | 1 | 10-Mar-14 | 10-Mar-14 | 14 |
| L05-6023 | Inspection of Exterior Framing | 0 | 0 | 10-Mar-14 | | 15 |
| L06-6008 | Frame Shaft Walls | 3 | 3 | 10-Mar-14 | 12-Mar-14 | 16 |
| L07-6008 | Frame Shaft Walls | 3 | 3 | 10-Mar-14 | 12-Mar-14 | 20 |
| L08-6008 | Frame Shaft Walls | 3 | 3 | 10-Mar-14 | 12-Mar-14 | 24 |
| L09-6008 | Frame Shaft Walls | 3 | 3 | 10-Mar-14 | 12-Mar-14 | 29 |
| L05-6011 | PreRock Shafts | 2 | 2 | 11-Mar-14 | 12-Mar-14 | 14 |
| L05-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 1 | 11-Mar-14 | 11-Mar-14 | 15 |
| L05-6010 | Frame Walls | 5 | 5 | 12-Mar-14 | 18-Mar-14 | 14 |
| L05-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 12-Mar-14 | 12-Mar-14 | 14 |
| L05-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 12-Mar-14 | 12-Mar-14 | 15 |
| L05-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 13-Mar-14 | 13-Mar-14 | 14 |
| L05-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 13-Mar-14 | 13-Mar-14 | 15 |
| L06-6004 | CMU Wall/Clips | 3 | 3 | 13-Mar-14 | 17-Mar-14 | 149 |
| L06-6009 | Inspect Shafts | 1 | 1 | 13-Mar-14 | 13-Mar-14 | 16 |

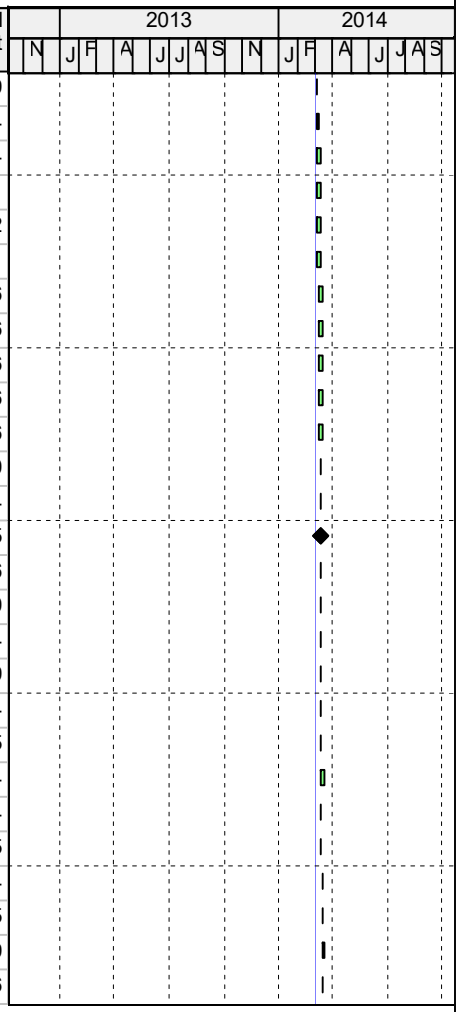



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6002 | Layout | 5 | 5 | 13-Mar-14 | 19-Mar-14 | 21 |
| L07-6009 | Inspect Shafts | 1 | 1 | 13-Mar-14 | 13-Mar-14 | 20 |
| L08-6009 | Inspect Shafts | 1 | 1 | 13-Mar-14 | 13-Mar-14 | 24 |
| L09-6009 | Inspect Shafts | 1 | 1 | 13-Mar-14 | 13-Mar-14 | 29 |
| L10-6008 | Frame Shaft Walls | 3 | 3 | 13-Mar-14 | 17-Mar-14 | 31 |
| L11-8219 | HVAC Risers | 5 | 5 | 13-Mar-14 | 19-Mar-14 | 147 |
| L11-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 13-Mar-14 | 19-Mar-14 | 31 |
| L05-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 14-Mar-14 | 14-Mar-14 | 15 |
| L06-6011 | PreRock Shafts | 2 | 2 | 14-Mar-14 | 17-Mar-14 | 16 |
| L07-6011 | PreRock Shafts | 2 | 2 | 14-Mar-14 | 17-Mar-14 | 20 |
| L08-6011 | PreRock Shafts | 2 | 2 | 14-Mar-14 | 17-Mar-14 | 24 |
| L09-6011 | PreRock Shafts | 2 | 2 | 14-Mar-14 | 17-Mar-14 | 29 |
| L05-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 17-Mar-14 | 17-Mar-14 | 15 |
| L06-6010 | Frame Walls | 5 | 5 | 17-Mar-14 | 21-Mar-14 | 16 |
| L06-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 17-Mar-14 | 17-Mar-14 | 16 |
| L06-6023 | Inspection of Exterior Framing | 0 | 0 | 17-Mar-14 | | 15 |
| L07-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 17-Mar-14 | 17-Mar-14 | 20 |
| L08-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 17-Mar-14 | 17-Mar-14 | 24 |
| L09-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 17-Mar-14 | 17-Mar-14 | 29 |
| L03-6009 | Inspect Shafts | 1 | 1 | 18-Mar-14 | 18-Mar-14 | 0 |
| L03-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 18-Mar-14 | 18-Mar-14 | 0 |
| L04-6009 | Inspect Shafts | 1 | 1 | 18-Mar-14 | 18-Mar-14 | 5 |
| L04-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 18-Mar-14 | 18-Mar-14 | 5 |
| L05-6012 | Fire Sprinkler Mains | 5 | 5 | 18-Mar-14 | 24-Mar-14 | 14 |
| L05-6014 | Set Tubs & Plumbing Rl | 5 | 5 | 18-Mar-14 | 24-Mar-14 | 14 |
| L05-6016 | Electrical Rl | 5 | 5 | 18-Mar-14 | 24-Mar-14 | 14 |
| L05-6018 | HVAC Rl | 5 | 5 | 18-Mar-14 | 24-Mar-14 | 14 |

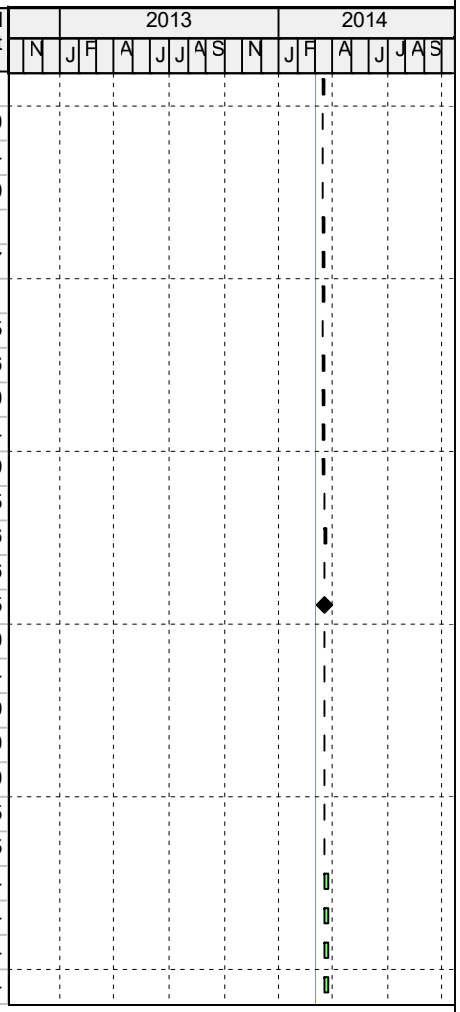



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6022 | Fire Alarm / Elec Specialties Rl | 5 | 5 | 18-Mar-14 | 24-Mar-14 | 14 |
| L05-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 18-Mar-14 | 18-Mar-14 | 15 |
| L06-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 18-Mar-14 | 18-Mar-14 | 16 |
| L06-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 18-Mar-14 | 18-Mar-14 | 15 |
| L07-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 18-Mar-14 | 18-Mar-14 | 20 |
| L08-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 18-Mar-14 | 18-Mar-14 | 24 |
| L09-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 18-Mar-14 | 18-Mar-14 | 29 |
| L10-6009 | Inspect Shafts | 1 | 1 | 18-Mar-14 | 18-Mar-14 | 31 |
| L03-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 19-Mar-14 | 19-Mar-14 | 0 |
| L04-6011 | PreRock Shafts | 2 | 2 | 19-Mar-14 | 20-Mar-14 | 7 |
| L04-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 19-Mar-14 | 19-Mar-14 | 5 |
| L05-6020 | Install Hollow Metal Frames | 3 | 3 | 19-Mar-14 | 21-Mar-14 | 18 |
| L05-6019 | Complete Top Out GWB | 2 | 2 | 19-Mar-14 | 20-Mar-14 | 14 |
| L05-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 19-Mar-14 | 24-Mar-14 | 15 |
| L06-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 19-Mar-14 | 19-Mar-14 | 15 |
| L10-6011 | PreRock Shafts | 2 | 2 | 19-Mar-14 | 20-Mar-14 | 31 |
| L03-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 20-Mar-14 | 20-Mar-14 | 2 |
| L03-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 20-Mar-14 | 20-Mar-14 | 0 |
| L04-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 20-Mar-14 | 20-Mar-14 | 7 |
| L04-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 20-Mar-14 | 20-Mar-14 | 5 |
| L05-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 20-Mar-14 | 24-Mar-14 | 14 |
| L05-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 20-Mar-14 | 21-Mar-14 | 15 |
| L06-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 20-Mar-14 | 20-Mar-14 | 15 |
| L07-6004 | CMU Wall/Clips | 3 | 3 | 20-Mar-14 | 24-Mar-14 | 144 |
| L08-6002 | Layout | 5 | 5 | 20-Mar-14 | 26-Mar-14 | 21 |
| L10-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 20-Mar-14 | 20-Mar-14 | 31 |
| L11-6008 | Frame Shaft Walls | 3 | 3 | 20-Mar-14 | 24-Mar-14 | 31 |

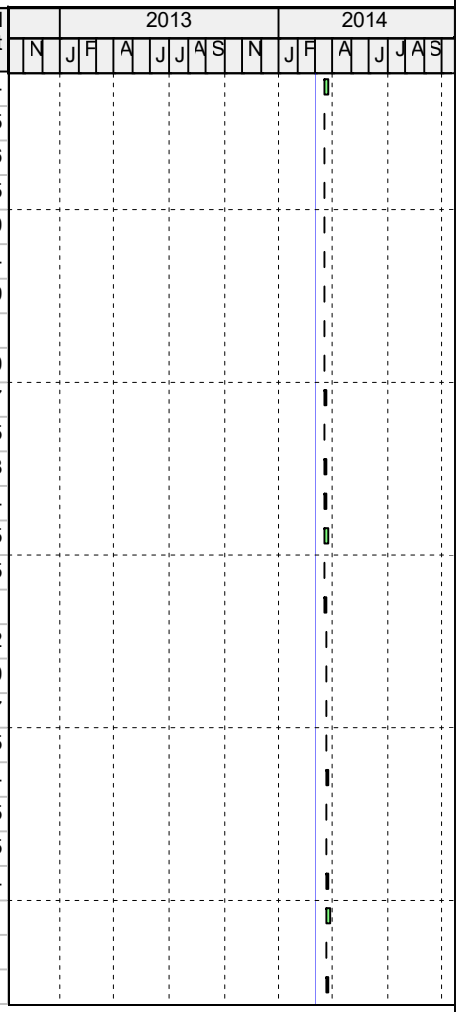



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8219 | HVAC Risers | 5 | 5 | 20-Mar-14 | 26-Mar-14 | 142 |
| L12-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 20-Mar-14 | 26-Mar-14 | 46 |
| L03-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 21-Mar-14 | 21-Mar-14 | 145 |
| L03-6019 | Complete Top Out GWB | 2 | 2 | 21-Mar-14 | 24-Mar-14 | 2 |
| L03-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 21-Mar-14 | 21-Mar-14 | 0 |
| L04-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 21-Mar-14 | 21-Mar-14 | 145 |
| L04-6019 | Complete Top Out GWB | 2 | 2 | 21-Mar-14 | 24-Mar-14 | 7 |
| L04-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 21-Mar-14 | 21-Mar-14 | 5 |
| L05-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 21-Mar-14 | 25-Mar-14 | 14 |
| L06-6012 | Fire Sprinkler Mains | 5 | 5 | 21-Mar-14 | 27-Mar-14 | 16 |
| L06-6014 | Set Tubs & Plumbing RI | 5 | 5 | 21-Mar-14 | 27-Mar-14 | 16 |
| L06-6016 | Electrical RI | 5 | 5 | 21-Mar-14 | 27-Mar-14 | 16 |
| L06-6018 | HVAC RI | 5 | 5 | 21-Mar-14 | 27-Mar-14 | 16 |
| L06-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 21-Mar-14 | 27-Mar-14 | 16 |
| L06-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 21-Mar-14 | 21-Mar-14 | 15 |
| L10-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 21-Mar-14 | 21-Mar-14 | 31 |
| L03-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 24-Mar-14 | 26-Mar-14 | 2 |
| L03-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 24-Mar-14 | 24-Mar-14 | 0 |
| L04-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 24-Mar-14 | 26-Mar-14 | 7 |
| L04-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 24-Mar-14 | 24-Mar-14 | 5 |
| L06-6020 | Install Hollow Metal Frames | 3 | 3 | 24-Mar-14 | 26-Mar-14 | 20 |
| L06-6019 | Complete Top Out GWB | 2 | 2 | 24-Mar-14 | 25-Mar-14 | 16 |
| L06-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 24-Mar-14 | 24-Mar-14 | 15 |
| L07-6010 | Frame Walls | 5 | 5 | 24-Mar-14 | 28-Mar-14 | 16 |
| L07-6023 | Inspection of Exterior Framing | 0 | 0 | 24-Mar-14 | | 15 |
| L03-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 25-Mar-14 | 27-Mar-14 | 2 |
| L03-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 25-Mar-14 | 25-Mar-14 | 0 |

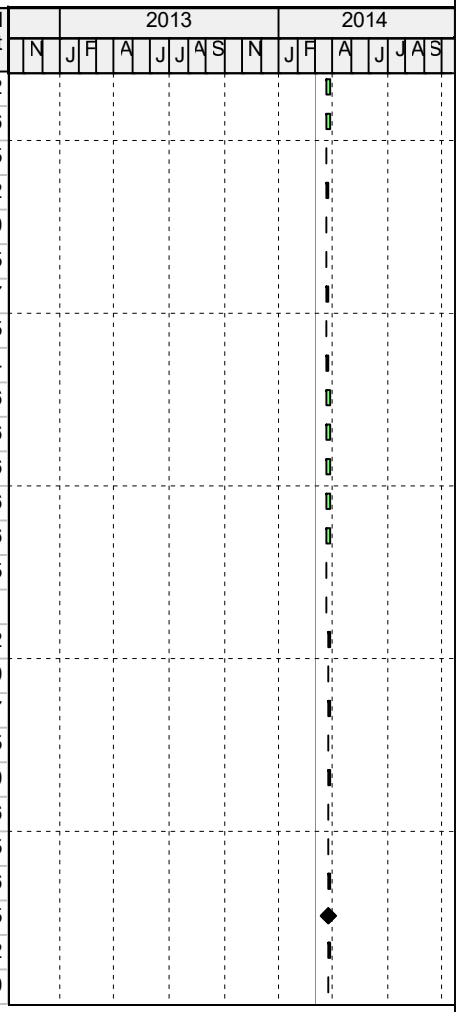



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 25-Mar-14 | 27-Mar-14 | 7 |
| L04-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 25-Mar-14 | 25-Mar-14 | 5 |
| L05-6024 | Inspections for GWB Cover | 1 | 1 | 25-Mar-14 | 25-Mar-14 | 14 |
| L06-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 25-Mar-14 | 27-Mar-14 | 16 |
| L06-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 25-Mar-14 | 25-Mar-14 | 15 |
| L07-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 25-Mar-14 | 25-Mar-14 | 15 |
| L11-6009 | Inspect Shafts | 1 | 1 | 25-Mar-14 | 25-Mar-14 | 31 |
| L03-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 26-Mar-14 | 31-Mar-14 | 0 |
| L04-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 26-Mar-14 | 31-Mar-14 | 5 |
| L06-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 26-Mar-14 | 28-Mar-14 | 16 |
| L06-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 26-Mar-14 | 31-Mar-14 | 15 |
| L07-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 26-Mar-14 | 26-Mar-14 | 15 |
| L11-6011 | PreRock Shafts | 2 | 2 | 26-Mar-14 | 27-Mar-14 | 31 |
| L03-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 27-Mar-14 | 28-Mar-14 | 0 |
| L04-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 27-Mar-14 | 28-Mar-14 | 5 |
| L06-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 27-Mar-14 | 28-Mar-14 | 15 |
| L07-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 27-Mar-14 | 27-Mar-14 | 15 |
| L08-6004 | CMU Wall/Clips | 3 | 3 | 27-Mar-14 | 31-Mar-14 | 139 |
| L09-6002 | Layout | 5 | 5 | 27-Mar-14 | 02-Apr-14 | 21 |
| L11-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 27-Mar-14 | 27-Mar-14 | 31 |
| L12-6008 | Frame Shaft Walls | 3 | 3 | 27-Mar-14 | 31-Mar-14 | 46 |
| L14-8219 | HVAC Risers | 5 | 5 | 27-Mar-14 | 02-Apr-14 | 137 |
| L14-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 27-Mar-14 | 02-Apr-14 | 46 |
| L07-6012 | Fire Sprinkler Mains | 5 | 5 | 28-Mar-14 | 03-Apr-14 | 16 |
| L07-6014 | Set Tubs & Plumbing RI | 5 | 5 | 28-Mar-14 | 03-Apr-14 | 16 |
| L07-6016 | Electrical RI | 5 | 5 | 28-Mar-14 | 03-Apr-14 | 16 |
| L07-6018 | HVAC RI | 5 | 5 | 28-Mar-14 | 03-Apr-14 | 16 |

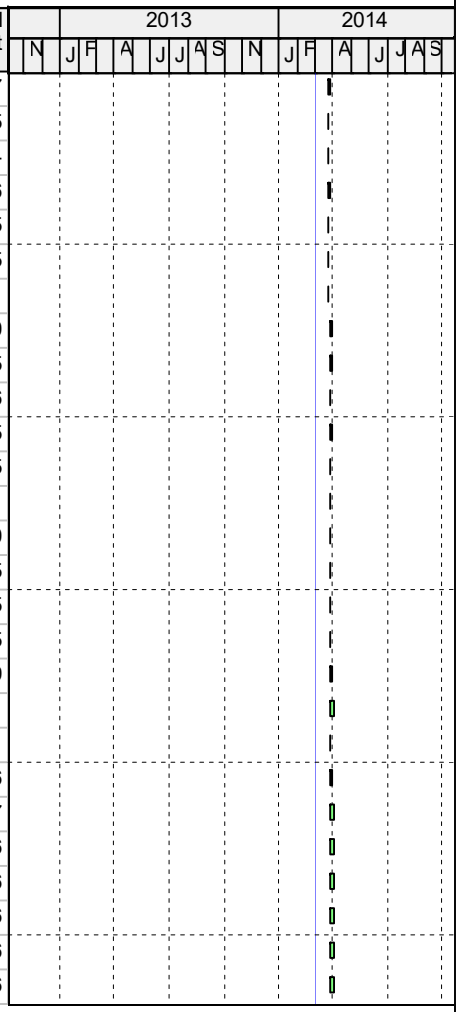



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6022 | Fire Alarm / Elec Specialties Rl | 5 | 5 | 28-Mar-14 | 03-Apr-14 | 16 |
| L07-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 28-Mar-14 | 28-Mar-14 | 15 |
| L11-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 28-Mar-14 | 28-Mar-14 | 31 |
| L03-6024 | Inspections for GWB Cover | 1 | 1 | 31-Mar-14 | 31-Mar-14 | 0 |
| L04-6024 | Inspections for GWB Cover | 1 | 1 | 31-Mar-14 | 31-Mar-14 | 5 |
| L06-6024 | Inspections for GWB Cover | 1 | 1 | 31-Mar-14 | 31-Mar-14 | 15 |
| L07-6020 | Install Hollow Metal Frames | 3 | 3 | 31-Mar-14 | 02-Apr-14 | 20 |
| L07-6019 | Complete Top Out GWB | 2 | 2 | 31-Mar-14 | 01-Apr-14 | 16 |
| L07-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 31-Mar-14 | 31-Mar-14 | 15 |
| L08-6010 | Frame Walls | 5 | 5 | 31-Mar-14 | 04-Apr-14 | 16 |
| L08-6023 | Inspection of Exterior Framing | 0 | 0 | 31-Mar-14 | | 15 |
| L07-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 01-Apr-14 | 03-Apr-14 | 16 |
| L07-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 01-Apr-14 | 01-Apr-14 | 15 |
| L08-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 1 | 01-Apr-14 | 01-Apr-14 | 15 |
| L12-6009 | Inspect Shafts | 1 | 1 | 01-Apr-14 | 01-Apr-14 | 46 |
| L07-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 02-Apr-14 | 04-Apr-14 | 16 |
| L07-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 02-Apr-14 | 07-Apr-14 | 15 |
| L08-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 02-Apr-14 | 02-Apr-14 | 15 |
| L12-6011 | PreRock Shafts | 2 | 2 | 02-Apr-14 | 03-Apr-14 | 46 |
| L07-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 03-Apr-14 | 04-Apr-14 | 15 |
| L08-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 03-Apr-14 | 03-Apr-14 | 15 |
| L09-6004 | CMU Wall/Clips | 3 | 3 | 03-Apr-14 | 07-Apr-14 | 134 |
| L12-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 03-Apr-14 | 03-Apr-14 | 46 |
| L14-6008 | Frame Shaft Walls | 3 | 3 | 03-Apr-14 | 07-Apr-14 | 46 |
| L15-8219 | HVAC Risers | 5 | 5 | 03-Apr-14 | 09-Apr-14 | 132 |
| L15-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 03-Apr-14 | 09-Apr-14 | 46 |
| L08-6012 | Fire Sprinkler Mains | 5 | 5 | 04-Apr-14 | 10-Apr-14 | 16 |

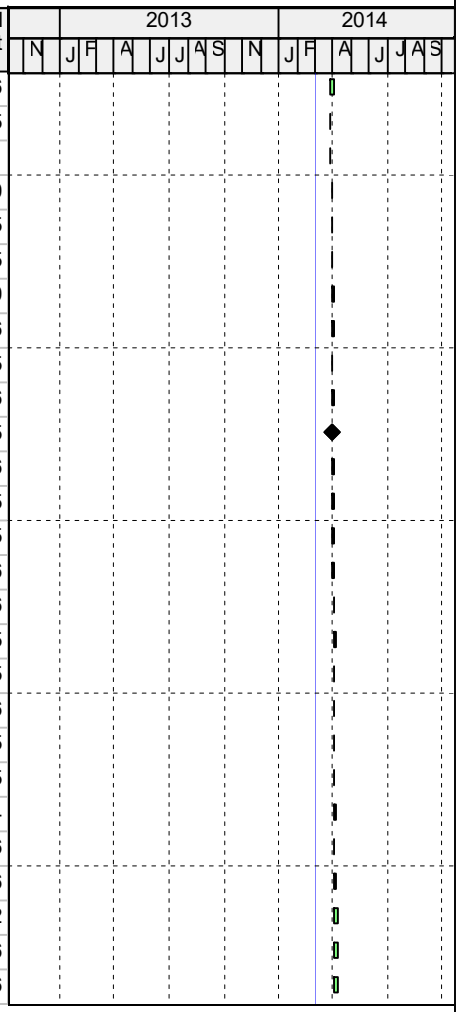



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-6014 | Set Tubs & Plumbing Rl | 5 | 5 | 04-Apr-14 | 10-Apr-14 | 16 |
| L08-6016 | Electrical Rl | 5 | 5 | 04-Apr-14 | 10-Apr-14 | 16 |
| L08-6018 | HVAC Rl | 5 | 5 | 04-Apr-14 | 10-Apr-14 | 16 |
| L08-6022 | Fire Alarm / Elec Specialties Rl | 5 | 5 | 04-Apr-14 | 10-Apr-14 | 16 |
| L08-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 04-Apr-14 | 04-Apr-14 | 15 |
| L10-6002 | Layout | 5 | 5 | 04-Apr-14 | 10-Apr-14 | 20 |
| L12-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 04-Apr-14 | 04-Apr-14 | 46 |
| L07-6024 | Inspections for GWB Cover | 1 | 1 | 07-Apr-14 | 07-Apr-14 | 15 |
| L08-6020 | Install Hollow Metal Frames | 3 | 3 | 07-Apr-14 | 09-Apr-14 | 20 |
| L08-6019 | Complete Top Out GWB | 2 | 2 | 07-Apr-14 | 08-Apr-14 | 16 |
| L08-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 07-Apr-14 | 07-Apr-14 | 15 |
| L09-6010 | Frame Walls | 5 | 5 | 07-Apr-14 | 11-Apr-14 | 16 |
| L09-6023 | Inspection of Exterior Framing | 0 | 0 | 07-Apr-14 | | 15 |
| L08-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 08-Apr-14 | 10-Apr-14 | 16 |
| L08-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 08-Apr-14 | 08-Apr-14 | 15 |
| L09-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 1 | 08-Apr-14 | 08-Apr-14 | 15 |
| L14-6009 | Inspect Shafts | 1 | 1 | 08-Apr-14 | 08-Apr-14 | 46 |
| L08-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 09-Apr-14 | 11-Apr-14 | 16 |
| L08-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 09-Apr-14 | 14-Apr-14 | 15 |
| L09-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 09-Apr-14 | 09-Apr-14 | 15 |
| L14-6011 | PreRock Shafts | 2 | 2 | 09-Apr-14 | 10-Apr-14 | 46 |
| L08-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 10-Apr-14 | 11-Apr-14 | 15 |
| L09-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 10-Apr-14 | 10-Apr-14 | 15 |
| L11-6002 | Layout | 5 | 5 | 10-Apr-14 | 16-Apr-14 | 21 |
| L14-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 10-Apr-14 | 10-Apr-14 | 46 |
| L15-6008 | Frame Shaft Walls | 3 | 3 | 10-Apr-14 | 14-Apr-14 | 46 |
| L16-8219 | HVAC Risers | 5 | 5 | 10-Apr-14 | 16-Apr-14 | 127 |

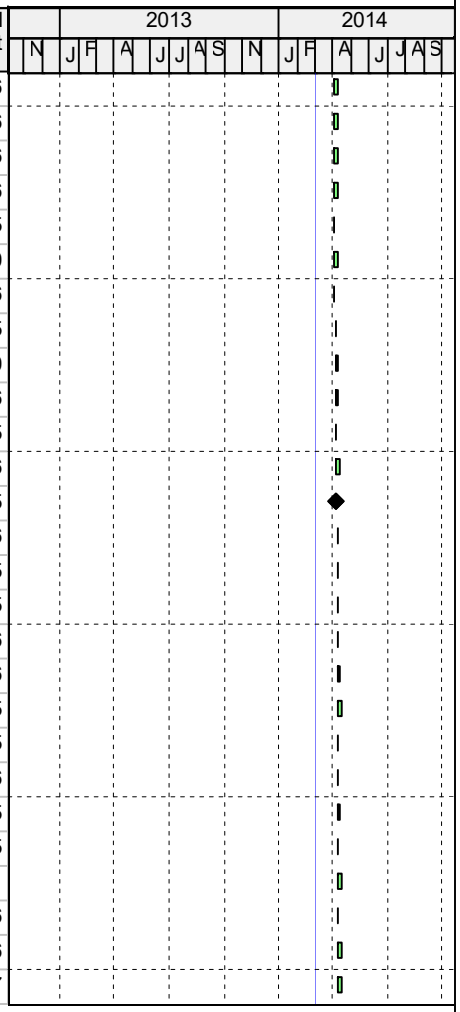



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 10-Apr-14 | 16-Apr-14 | 46 |
| L03-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 11-Apr-14 | 21-Apr-14 | 80 |
| L09-6012 | Fire Sprinkler Mains | 5 | 5 | 11-Apr-14 | 17-Apr-14 | 16 |
| L09-6014 | Set Tubs & Plumbing RI | 5 | 5 | 11-Apr-14 | 17-Apr-14 | 16 |
| L09-6016 | Electrical RI | 5 | 5 | 11-Apr-14 | 17-Apr-14 | 16 |
| L09-6018 | HVAC RI | 5 | 5 | 11-Apr-14 | 17-Apr-14 | 16 |
| L09-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 11-Apr-14 | 17-Apr-14 | 16 |
| L09-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 11-Apr-14 | 11-Apr-14 | 15 |
| L10-6004 | CMU Wall/Clips | 3 | 3 | 11-Apr-14 | 15-Apr-14 | 128 |
| L14-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 11-Apr-14 | 11-Apr-14 | 46 |
| L08-6024 | Inspections for GWB Cover | 1 | 1 | 14-Apr-14 | 14-Apr-14 | 15 |
| L09-6020 | Install Hollow Metal Frames | 3 | 3 | 14-Apr-14 | 16-Apr-14 | 20 |
| L09-6019 | Complete Top Out GWB | 2 | 2 | 14-Apr-14 | 15-Apr-14 | 16 |
| L09-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 14-Apr-14 | 14-Apr-14 | 15 |
| L10-6010 | Frame Walls | 5 | 5 | 14-Apr-14 | 18-Apr-14 | 16 |
| L10-6023 | Inspection of Exterior Framing | 0 | 0 | 14-Apr-14 | | 15 |
| L09-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 15-Apr-14 | 17-Apr-14 | 16 |
| L09-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 15-Apr-14 | 15-Apr-14 | 15 |
| L10-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 15-Apr-14 | 15-Apr-14 | 15 |
| L15-6009 | Inspect Shafts | 1 | 1 | 15-Apr-14 | 15-Apr-14 | 46 |
| L09-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 16-Apr-14 | 18-Apr-14 | 16 |
| L09-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 16-Apr-14 | 21-Apr-14 | 15 |
| L10-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 16-Apr-14 | 16-Apr-14 | 15 |
| L15-6011 | PreRock Shafts | 2 | 2 | 16-Apr-14 | 17-Apr-14 | 46 |
| L09-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 17-Apr-14 | 18-Apr-14 | 15 |
| L10-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 17-Apr-14 | 17-Apr-14 | 15 |
| L11-6004 | CMU Wall/Clips | 3 | 3 | 17-Apr-14 | 21-Apr-14 | 124 |

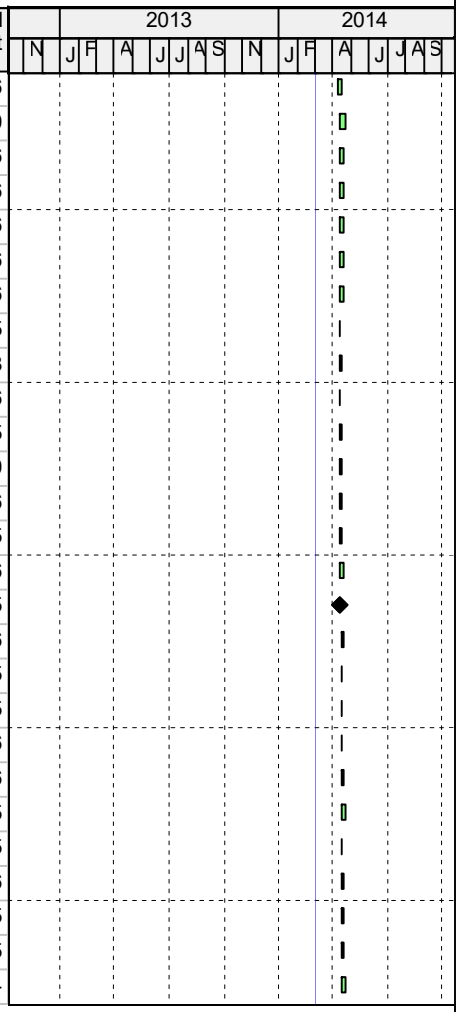



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 17-Apr-14 | 17-Apr-14 | 46 |
| L16-6008 | Frame Shaft Walls | 3 | 3 | 17-Apr-14 | 21-Apr-14 | 46 |
| L04-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 18-Apr-14 | 28-Apr-14 | 75 |
| L10-6012 | Fire Sprinkler Mains | 5 | 5 | 18-Apr-14 | 24-Apr-14 | 16 |
| L10-6014 | Set Tubs & Plumbing RI | 5 | 5 | 18-Apr-14 | 24-Apr-14 | 16 |
| L10-6016 | Electrical RI | 5 | 5 | 18-Apr-14 | 24-Apr-14 | 16 |
| L10-6018 | HVAC RI | 5 | 5 | 18-Apr-14 | 24-Apr-14 | 16 |
| L10-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 18-Apr-14 | 24-Apr-14 | 16 |
| L10-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 18-Apr-14 | 18-Apr-14 | 15 |
| L15-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 18-Apr-14 | 18-Apr-14 | 46 |
| L09-6024 | Inspections for GWB Cover | 1 | 1 | 21-Apr-14 | 21-Apr-14 | 15 |
| L10-6020 | Install Hollow Metal Frames | 3 | 3 | 21-Apr-14 | 23-Apr-14 | 20 |
| L10-6019 | Complete Top Out GWB | 2 | 2 | 21-Apr-14 | 22-Apr-14 | 16 |
| L10-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 21-Apr-14 | 21-Apr-14 | 15 |
| L11-6010 | Frame Walls | 5 | 5 | 21-Apr-14 | 25-Apr-14 | 16 |
| L11-6023 | Inspection of Exterior Framing | 0 | 0 | 21-Apr-14 | | 15 |
| L10-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 22-Apr-14 | 24-Apr-14 | 16 |
| L10-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 22-Apr-14 | 22-Apr-14 | 15 |
| L11-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 22-Apr-14 | 22-Apr-14 | 15 |
| L16-6009 | Inspect Shafts | 1 | 1 | 22-Apr-14 | 22-Apr-14 | 46 |
| L10-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 23-Apr-14 | 25-Apr-14 | 16 |
| L10-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 23-Apr-14 | 28-Apr-14 | 15 |
| L11-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 23-Apr-14 | 23-Apr-14 | 15 |
| L16-6011 | PreRock Shafts | 2 | 2 | 23-Apr-14 | 24-Apr-14 | 46 |
| L10-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 24-Apr-14 | 25-Apr-14 | 15 |
| L11-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 24-Apr-14 | 24-Apr-14 | 15 |
| L12-6002 | Layout | 5 | 5 | 24-Apr-14 | 30-Apr-14 | 31 |

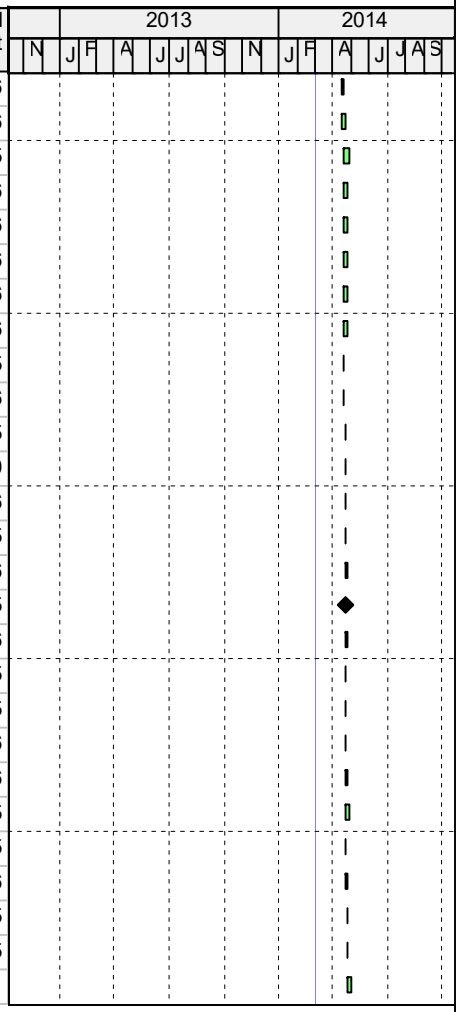



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 24-Apr-14 | 24-Apr-14 | 46 |
| L17-8219 | HVAC Risers | 5 | 5 | 24-Apr-14 | 30-Apr-14 | 117 |
| L17-8220 | Plumbing Mains/Risers/Overhead | 5 | 5 | 24-Apr-14 | 30-Apr-14 | 41 |
| L05-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 25-Apr-14 | 05-May-14 | 70 |
| L11-6012 | Fire Sprinkler Mains | 5 | 5 | 25-Apr-14 | 01-May-14 | 16 |
| L11-6014 | Set Tubs & Plumbing RI | 5 | 5 | 25-Apr-14 | 01-May-14 | 16 |
| L11-6016 | Electrical RI | 5 | 5 | 25-Apr-14 | 01-May-14 | 16 |
| L11-6018 | HVAC RI | 5 | 5 | 25-Apr-14 | 01-May-14 | 16 |
| L11-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 25-Apr-14 | 01-May-14 | 16 |
| L11-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 25-Apr-14 | 25-Apr-14 | 15 |
| L16-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 25-Apr-14 | 25-Apr-14 | 46 |
| L10-6024 | Inspections for GWB Cover | 1 | 1 | 28-Apr-14 | 28-Apr-14 | 15 |
| L11-6020 | Install Hollow Metal Frames | 3 | 3 | 28-Apr-14 | 30-Apr-14 | 20 |
| L11-6019 | Complete Top Out GWB | 2 | 2 | 28-Apr-14 | 29-Apr-14 | 16 |
| L11-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 28-Apr-14 | 28-Apr-14 | 15 |
| L14-6002 | Layout | 5 | 5 | 28-Apr-14 | 02-May-14 | 34 |
| L11-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 29-Apr-14 | 01-May-14 | 16 |
| L11-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 29-Apr-14 | 29-Apr-14 | 15 |
| L11-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 30-Apr-14 | 02-May-14 | 16 |
| L11-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 30-Apr-14 | 05-May-14 | 15 |
| L15-6002 | Layout | 5 | 5 | 30-Apr-14 | 06-May-14 | 37 |
| L11-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 01-May-14 | 02-May-14 | 15 |
| L12-6004 | CMU Wall/Clips | 3 | 3 | 01-May-14 | 05-May-14 | 114 |
| L17-6008 | Frame Shaft Walls | 3 | 3 | 01-May-14 | 05-May-14 | 41 |
| L06-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 02-May-14 | 12-May-14 | 65 |
| L16-6002 | Layout | 5 | 5 | 02-May-14 | 08-May-14 | 40 |
| L11-6024 | Inspections for GWB Cover | 1 | 1 | 05-May-14 | 05-May-14 | 15 |

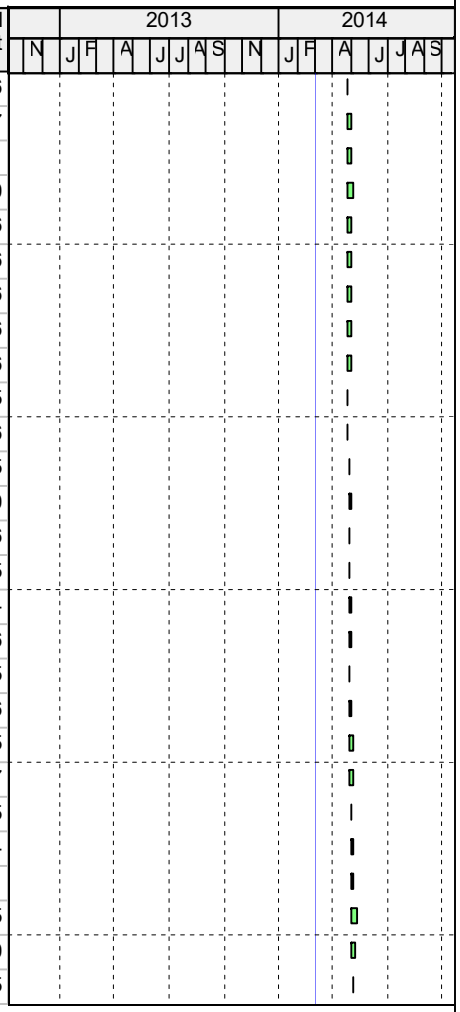



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-6010 | Frame Walls | 5 | 5 | 05-May-14 | 09-May-14 | 26 |
| L12-6023 | Inspection of Exterior Framing | 0 | 0 | 05-May-14 | | 25 |
| L14-6004 | CMU Wall/Clips | 3 | 3 | 05-May-14 | 07-May-14 | 112 |
| L12-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 06-May-14 | 06-May-14 | 25 |
| L17-6002 | Layout | 5 | 5 | 06-May-14 | 12-May-14 | 37 |
| L17-6009 | Inspect Shafts | 1 | 1 | 06-May-14 | 06-May-14 | 41 |
| L12-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 07-May-14 | 07-May-14 | 25 |
| L15-6004 | CMU Wall/Clips | 3 | 3 | 07-May-14 | 09-May-14 | 110 |
| L17-6011 | PreRock Shafts | 2 | 2 | 07-May-14 | 08-May-14 | 41 |
| L12-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 08-May-14 | 08-May-14 | 25 |
| L17-6015 | Inspect Pre Rock @ Shafts | 1 | 1 | 08-May-14 | 08-May-14 | 41 |
| L07-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 09-May-14 | 19-May-14 | 60 |
| L12-6012 | Fire Sprinkler Mains | 5 | 5 | 09-May-14 | 15-May-14 | 26 |
| L12-6014 | Set Tubs & Plumbing Rl | 5 | 5 | 09-May-14 | 15-May-14 | 26 |
| L12-6016 | Electrical Rl | 5 | 5 | 09-May-14 | 15-May-14 | 26 |
| L12-6018 | HVAC Rl | 5 | 5 | 09-May-14 | 15-May-14 | 26 |
| L12-6022 | Fire Alarm / Elec Specialties Rl | 5 | 5 | 09-May-14 | 15-May-14 | 26 |
| L12-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 09-May-14 | 09-May-14 | 25 |
| L16-6004 | CMU Wall/Clips | 3 | 3 | 09-May-14 | 13-May-14 | 108 |
| L17-6017 | Firetape/Caulk @ Shafts | 1 | 1 | 09-May-14 | 09-May-14 | 41 |
| L12-6020 | Install Hollow Metal Frames | 3 | 3 | 12-May-14 | 14-May-14 | 30 |
| L12-6019 | Complete Top Out GWB | 2 | 2 | 12-May-14 | 13-May-14 | 26 |
| L12-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 12-May-14 | 12-May-14 | 25 |
| L14-6010 | Frame Walls | 5 | 5 | 12-May-14 | 16-May-14 | 26 |
| L14-6023 | Inspection of Exterior Framing | 0 | 0 | 12-May-14 | | 25 |
| L12-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 13-May-14 | 15-May-14 | 26 |
| L12-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 13-May-14 | 13-May-14 | 25 |

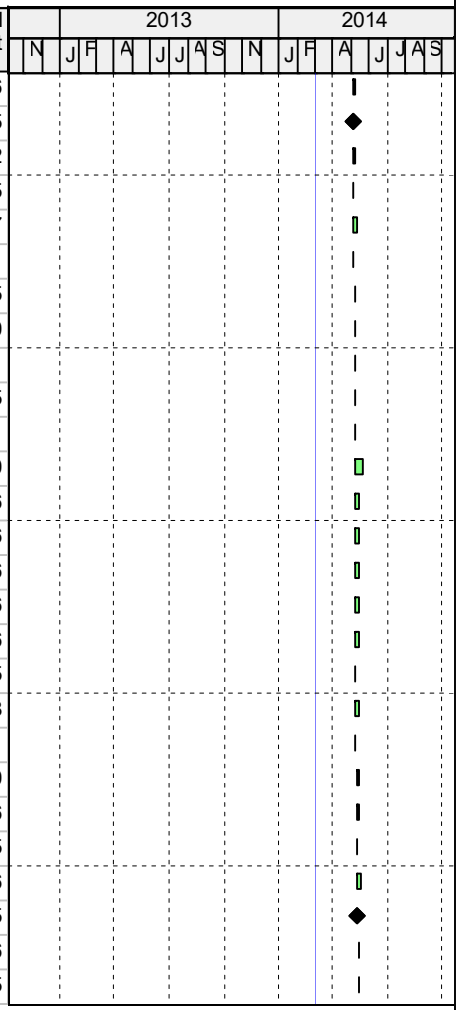



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 13-May-14 | 13-May-14 | 25 |
| L17-6004 | CMU Wall/Clips | 3 | 3 | 13-May-14 | 15-May-14 | 106 |
| L12-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 14-May-14 | 16-May-14 | 26 |
| L12-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 14-May-14 | 19-May-14 | 25 |
| L14-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 14-May-14 | 14-May-14 | 25 |
| L12-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 15-May-14 | 16-May-14 | 25 |
| L14-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 15-May-14 | 15-May-14 | 25 |
| L08-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 16-May-14 | 27-May-14 | 55 |
| L14-6012 | Fire Sprinkler Mains | 5 | 5 | 16-May-14 | 22-May-14 | 26 |
| L14-6014 | Set Tubs & Plumbing RI | 5 | 5 | 16-May-14 | 22-May-14 | 26 |
| L14-6016 | Electrical RI | 5 | 5 | 16-May-14 | 22-May-14 | 26 |
| L14-6018 | HVAC RI | 5 | 5 | 16-May-14 | 22-May-14 | 26 |
| L14-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 16-May-14 | 22-May-14 | 26 |
| L14-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 16-May-14 | 16-May-14 | 25 |
| L12-6024 | Inspections for GWB Cover | 1 | 1 | 19-May-14 | 19-May-14 | 25 |
| L14-6020 | Install Hollow Metal Frames | 3 | 3 | 19-May-14 | 21-May-14 | 30 |
| L14-6019 | Complete Top Out GWB | 2 | 2 | 19-May-14 | 20-May-14 | 26 |
| L14-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 19-May-14 | 19-May-14 | 25 |
| L15-6010 | Frame Walls | 5 | 5 | 19-May-14 | 23-May-14 | 26 |
| L15-6023 | Inspection of Exterior Framing | 0 | 0 | 19-May-14 | | 25 |
| L14-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 20-May-14 | 22-May-14 | 26 |
| L14-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 20-May-14 | 20-May-14 | 25 |
| L15-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 20-May-14 | 20-May-14 | 25 |
| L14-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 21-May-14 | 23-May-14 | 26 |
| L14-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 21-May-14 | 27-May-14 | 25 |
| L15-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 21-May-14 | 21-May-14 | 25 |
| L14-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 22-May-14 | 23-May-14 | 25 |

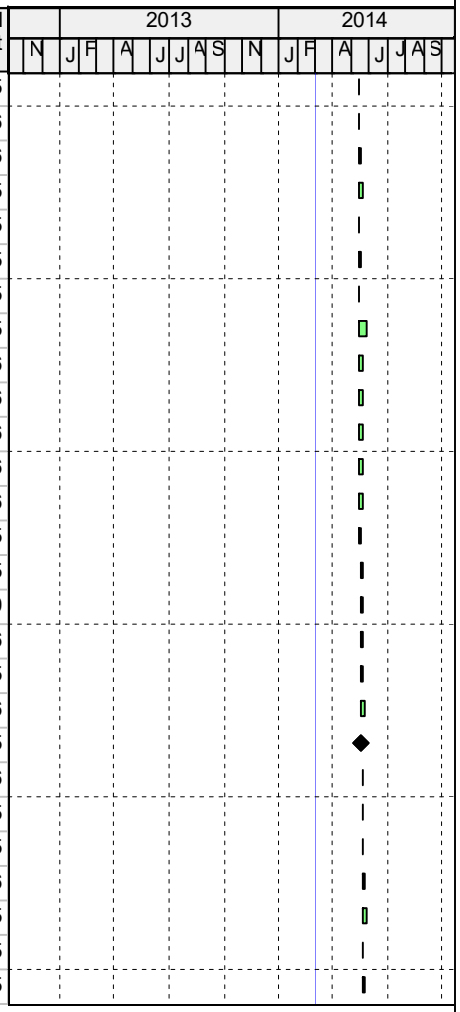



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 22-May-14 | 22-May-14 | 25 |
| L09-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 23-May-14 | 03-Jun-14 | 50 |
| L15-6012 | Fire Sprinkler Mains | 5 | 5 | 23-May-14 | 30-May-14 | 26 |
| L15-6014 | Set Tubs & Plumbing RI | 5 | 5 | 23-May-14 | 30-May-14 | 26 |
| L15-6016 | Electrical RI | 5 | 5 | 23-May-14 | 30-May-14 | 26 |
| L15-6018 | HVAC RI | 5 | 5 | 23-May-14 | 30-May-14 | 26 |
| L15-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 23-May-14 | 30-May-14 | 26 |
| L15-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 23-May-14 | 23-May-14 | 25 |
| L14-6024 | Inspections for GWB Cover | 1 | 1 | 27-May-14 | 27-May-14 | 25 |
| L15-6020 | Install Hollow Metal Frames | 3 | 3 | 27-May-14 | 29-May-14 | 30 |
| L15-6019 | Complete Top Out GWB | 2 | 2 | 27-May-14 | 28-May-14 | 26 |
| L15-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 27-May-14 | 27-May-14 | 25 |
| L16-6010 | Frame Walls | 5 | 5 | 27-May-14 | 02-Jun-14 | 26 |
| L16-6023 | Inspection of Exterior Framing | 0 | 0 | 27-May-14 | | 25 |
| L15-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 28-May-14 | 30-May-14 | 26 |
| L15-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 28-May-14 | 28-May-14 | 25 |
| L16-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 28-May-14 | 28-May-14 | 25 |
| L15-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 29-May-14 | 02-Jun-14 | 26 |
| L15-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 29-May-14 | 03-Jun-14 | 25 |
| L16-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 29-May-14 | 29-May-14 | 25 |
| L15-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 30-May-14 | 02-Jun-14 | 25 |
| L16-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 30-May-14 | 30-May-14 | 25 |
| L10-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 02-Jun-14 | 10-Jun-14 | 45 |
| L16-6012 | Fire Sprinkler Mains | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 26 |
| L16-6014 | Set Tubs & Plumbing RI | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 26 |
| L16-6016 | Electrical RI | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 26 |
| L16-6018 | HVAC RI | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 26 |

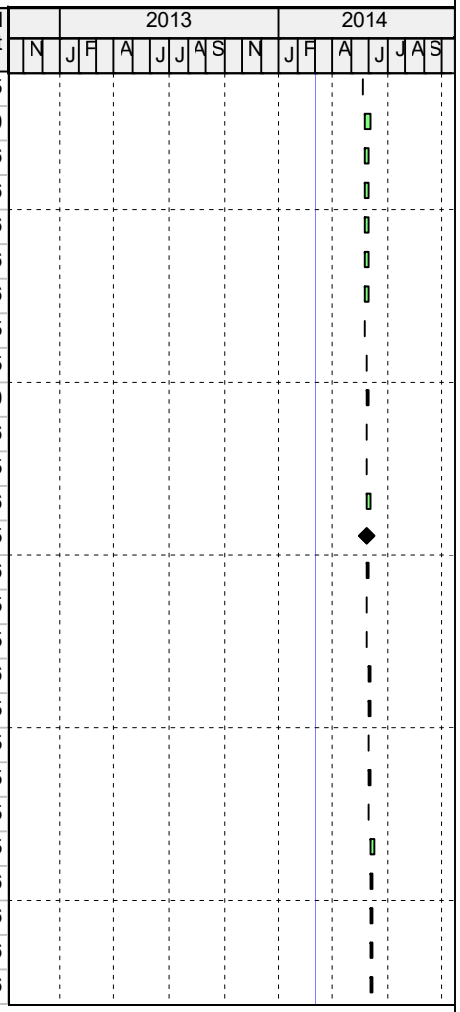



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6022 | Fire Alarm / Elec Specialties Rl | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 26 |
| L16-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 02-Jun-14 | 02-Jun-14 | 25 |
| L17-6010 | Frame Walls | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 27 |
| L17-6023 | Inspection of Exterior Framing | 0 | 0 | 02-Jun-14 | | 26 |
| L15-6024 | Inspections for GWB Cover | 1 | 1 | 03-Jun-14 | 03-Jun-14 | 25 |
| L16-6020 | Install Hollow Metal Frames | 3 | 3 | 03-Jun-14 | 05-Jun-14 | 30 |
| L16-6019 | Complete Top Out GWB | 2 | 2 | 03-Jun-14 | 04-Jun-14 | 26 |
| L16-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 03-Jun-14 | 03-Jun-14 | 25 |
| L17-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 03-Jun-14 | 03-Jun-14 | 26 |
| L16-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 04-Jun-14 | 06-Jun-14 | 26 |
| L16-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 04-Jun-14 | 04-Jun-14 | 25 |
| L17-6026 | Inspection of Thermal & VB @ Corners (Heat Pump) | 1 | 1 | 04-Jun-14 | 04-Jun-14 | 26 |
| L16-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 05-Jun-14 | 09-Jun-14 | 26 |
| L16-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 05-Jun-14 | 10-Jun-14 | 25 |
| L17-6028 | PreRock @ Corners (Heat Pump) | 1 | 1 | 05-Jun-14 | 05-Jun-14 | 26 |
| L16-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 06-Jun-14 | 09-Jun-14 | 25 |
| L17-6012 | Fire Sprinkler Mains | 5 | 5 | 06-Jun-14 | 12-Jun-14 | 27 |
| L17-6014 | Set Tubs & Plumbing Rl | 5 | 5 | 06-Jun-14 | 12-Jun-14 | 27 |
| L17-6016 | Electrical Rl | 5 | 5 | 06-Jun-14 | 12-Jun-14 | 27 |
| L17-6018 | HVAC Rl | 5 | 5 | 06-Jun-14 | 12-Jun-14 | 27 |
| L17-6022 | Fire Alarm / Elec Specialties Rl | 5 | 5 | 06-Jun-14 | 12-Jun-14 | 27 |
| L17-6029 | Inspection of PreRock@ Corners (Heat Pump) | 1 | 1 | 06-Jun-14 | 06-Jun-14 | 26 |
| L11-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 09-Jun-14 | 17-Jun-14 | 0 |
| L17-6020 | Install Hollow Metal Frames | 3 | 3 | 09-Jun-14 | 11-Jun-14 | 31 |
| L17-6019 | Complete Top Out GWB | 2 | 2 | 09-Jun-14 | 10-Jun-14 | 27 |
| L17-6030 | Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 09-Jun-14 | 09-Jun-14 | 26 |
| L16-6024 | Inspections for GWB Cover | 1 | 1 | 10-Jun-14 | 10-Jun-14 | 25 |

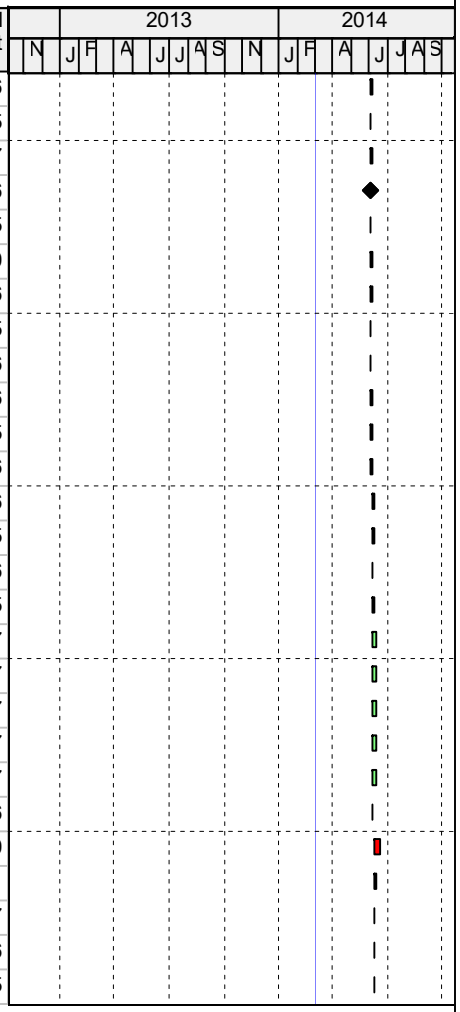



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 10-Jun-14 | 12-Jun-14 | 27 |
| L17-6031 | Inspection of Tape/Firecaulk @ Corners (Heat Pump) | 1 | 1 | 10-Jun-14 | 10-Jun-14 | 26 |
| L17-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 11-Jun-14 | 13-Jun-14 | 27 |
| L17-6019HP | Install Heat Pumps/Sweat Fittings | 4 | 4 | 11-Jun-14 | 16-Jun-14 | 26 |
| L17-6032 | Install Prefabbed Remainder of Walls | 2 | 2 | 12-Jun-14 | 13-Jun-14 | 26 |
| L12-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 16-Jun-14 | 24-Jun-14 | 35 |
| L17-6024 | Inspections for GWB Cover | 1 | 1 | 16-Jun-14 | 16-Jun-14 | 26 |
| L14-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 23-Jun-14 | 01-Jul-14 | 30 |
| L15-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 30-Jun-14 | 09-Jul-14 | 25 |
| L16-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 08-Jul-14 | 16-Jul-14 | 20 |
| L17-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 15-Jul-14 | 23-Jul-14 | 15 |
| **Mechanical Penthouse** | | | | | | |
| PH-6002 | PH - Layout | 1 | 1 | 13-May-14 | 13-May-14 | 37 |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 5 | 14-May-14 | 20-May-14 | 48 |
| PH-6006 | PH - Ext Wall Framing - (Incldg Roof Parapet) | 10 | 10 | 14-May-14 | 28-May-14 | 37 |
| PH-6008 | PH - Int Wall Framing | 3 | 3 | 29-May-14 | 02-Jun-14 | 37 |
| PH-6012 | PH - Fire Sprinkler RI | 8 | 8 | 03-Jun-14 | 12-Jun-14 | 44 |
| PH-6014 | PH - Plumbing RI | 12 | 12 | 03-Jun-14 | 18-Jun-14 | 40 |
| PH-6016 | PH - Electrical RI | 12 | 12 | 03-Jun-14 | 18-Jun-14 | 40 |
| PH-6018 | PH - HVAC RI | 15 | 15 | 03-Jun-14 | 23-Jun-14 | 37 |
| PH-6020 | PH - H Mtl Frames | 2 | 2 | 03-Jun-14 | 04-Jun-14 | 55 |
| PH-6022 | PH - Fire Alarm / Elec Specialties RI | 5 | 5 | 03-Jun-14 | 09-Jun-14 | 90 |
| PH-6024 | PH - Inspections | 2 | 2 | 24-Jun-14 | 25-Jun-14 | 37 |
| **Finishes** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |

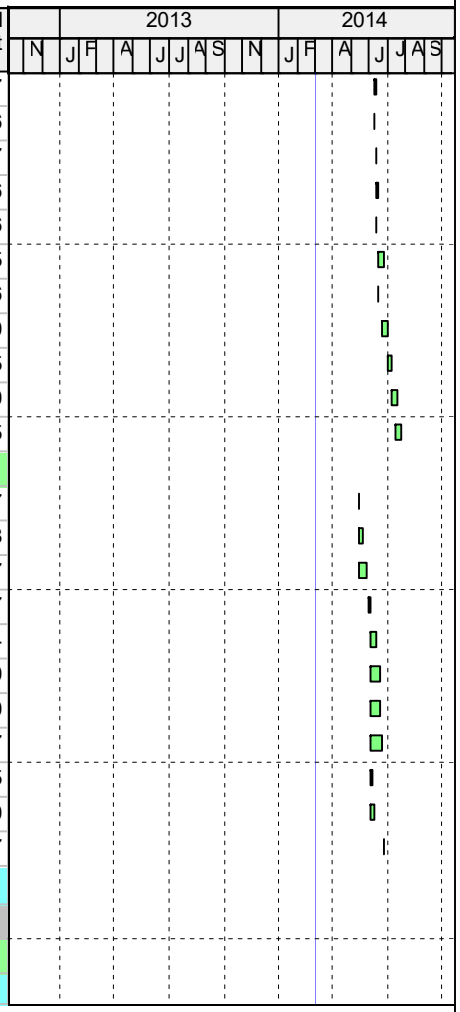



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8100 | LL4 - Insulation | 2 | 2 | 19-May-14 | 20-May-14 | 8 |
| LL4-8102 | LL4 - GWB Hang / Tape / Finish | 12 | 12 | 21-May-14 | 06-Jun-14 | 48 |
| LL4-8104 | LL4 - Int Painting | 3 | 3 | 04-Jun-14 | 06-Jun-14 | 56 |
| LL4-8108 | LL4 - Elec Trim / Finish | 6 | 6 | 09-Jun-14 | 16-Jun-14 | 57 |
| LL4-8110 | LL4 - HVAC Trim / Finish | 6 | 6 | 09-Jun-14 | 16-Jun-14 | 57 |
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 5 | 5 | 09-Jun-14 | 13-Jun-14 | 58 |
| LL4-8114 | LL4 - Striping / Signage | 3 | 3 | 09-Jun-14 | 11-Jun-14 | 69 |
| LL4-8118 | LL4 - Elec Specialties Trim / Finish | 4 | 4 | 09-Jun-14 | 12-Jun-14 | 59 |
| LL4-8122 | LL4 - Plumbing Trim / Finish | 5 | 5 | 17-Jun-14 | 23-Jun-14 | 56 |
| LL4-8124 | LL4 - Flooring | 3 | 3 | 17-Jun-14 | 19-Jun-14 | 57 |
| LL4-8126 | LL4 - Doors & Hardware | 3 | 3 | 18-Jun-14 | 20-Jun-14 | 57 |
| LL4-8130 | LL4 - Substantially Complete | 0 | 0 | | 23-Jun-14 | 56 |
| LL4-8132 | LL4 - Contractor Pre-Punchlist | 5 | 5 | 24-Jun-14 | 30-Jun-14 | 59 |
| LL4-8134 | LL4 - Pre-Clean | 5 | 5 | 24-Jun-14 | 30-Jun-14 | 56 |
| LL4-8208 | LL4 - Final Clean | 3 | 3 | 01-Jul-14 | 03-Jul-14 | 56 |
| LL4-8210 | LL4 - Owner Walk / Create Punchlist | 1 | 1 | 07-Jul-14 | 07-Jul-14 | 56 |
| LL4-8212 | LL4 - Final Punchlist | 5 | 5 | 08-Jul-14 | 14-Jul-14 | 56 |
| LL4-8214 | LL4 - Floor Complete | 0 | 0 | | 14-Jul-14 | 56 |
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL3-8100 | LL3 - Insulation | 2 | 2 | 27-May-14 | 28-May-14 | 8 |
| LL3-8102 | LL3 - GWB Hang / Tape / Finish | 12 | 12 | 29-May-14 | 13-Jun-14 | 46 |
| LL3-8104 | LL3 - Int Painting | 3 | 3 | 11-Jun-14 | 13-Jun-14 | 56 |
| LL3-8108 | LL3 - Elec Trim / Finish | 6 | 6 | 16-Jun-14 | 23-Jun-14 | 57 |
| LL3-8110 | LL3 - HVAC Trim / Finish | 6 | 6 | 16-Jun-14 | 23-Jun-14 | 57 |
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 5 | 5 | 16-Jun-14 | 20-Jun-14 | 58 |
| LL3-8114 | LL3 - Striping / Signage | 3 | 3 | 16-Jun-14 | 18-Jun-14 | 69 |

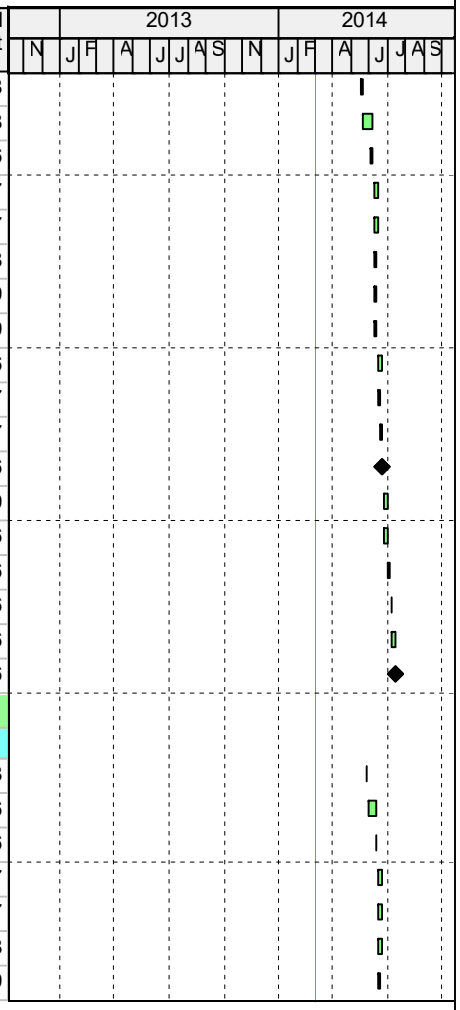



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-8118 | LL3 - Elec Specialties Trim / Finish | 4 | 4 | 16-Jun-14 | 19-Jun-14 | 59 |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 5 | 5 | 24-Jun-14 | 30-Jun-14 | 56 |
| LL3-8124 | LL3 - Flooring | 3 | 3 | 24-Jun-14 | 26-Jun-14 | 57 |
| LL3-8126 | LL3 - Doors & Hardware | 3 | 3 | 25-Jun-14 | 27-Jun-14 | 57 |
| LL3-8130 | LL3 - Substantially Complete | 0 | 0 | | 30-Jun-14 | 56 |
| LL3-8132 | LL3 - Contractor Pre-Punchlist | 5 | 5 | 01-Jul-14 | 08-Jul-14 | 59 |
| LL3-8134 | LL3 - Pre-Clean | 5 | 5 | 01-Jul-14 | 08-Jul-14 | 56 |
| LL3-8208 | LL3 - Final Clean | 3 | 3 | 09-Jul-14 | 11-Jul-14 | 56 |
| LL3-8210 | LL3 - Owner Walk / Create Punchlist | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 56 |
| LL3-8212 | LL3 - Final Punchlist | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 56 |
| LL3-8214 | LL3 - Floor Complete | 0 | 0 | | 21-Jul-14 | 56 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL2E-8102 | LL2 - GWB Hang / Tape / Finish @ Electrical Rooms | 8 | 8 | 15-Apr-14 | 24-Apr-14 | 121 |
| LL2-8100 | LL2 - Insulation | 5 | 5 | 03-Jun-14 | 09-Jun-14 | 8 |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish | 15 | 15 | 10-Jun-14 | 30-Jun-14 | 41 |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 10 | 10 | 10-Jun-14 | 23-Jun-14 | 51 |
| LL2-8104 | LL2 - Int Painting | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 41 |
| LL2-8120 | LL2 - Steel Pipe Guardrails | 6 | 6 | 01-Jul-14 | 09-Jul-14 | 55 |
| LL2-8108 | LL2 - Elec Trim / Finish | 10 | 10 | 03-Jul-14 | 17-Jul-14 | 43 |
| LL2-8110 | LL2 - HVAC Trim / Finish | 12 | 12 | 03-Jul-14 | 21-Jul-14 | 41 |
| LL2-8112 | LL2 - Fire Sprinkler Trim / Finish | 8 | 8 | 03-Jul-14 | 15-Jul-14 | 45 |
| LL2-8116 | LL2 - Finish Carpentry / Millwork | 2 | 2 | 03-Jul-14 | 07-Jul-14 | 50 |
| LL2-8118 | LL2 - Elec Specialties Trim / Finish | 4 | 4 | 03-Jul-14 | 09-Jul-14 | 49 |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 9 | 9 | 03-Jul-14 | 16-Jul-14 | 50 |
| LL2-8128 | LL2 - Entry Gates | 3 | 3 | 09-Jul-14 | 11-Jul-14 | 51 |
| LL2-8122 | LL2 - Plumbing Trim / Finish | 5 | 5 | 10-Jul-14 | 16-Jul-14 | 50 |

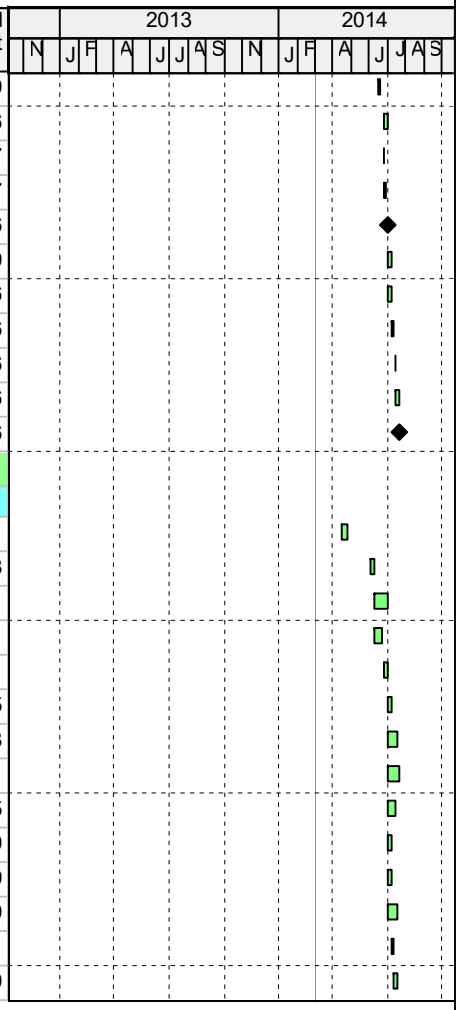



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-8114 | LL2 - Striping / Signage | 3 | 3 | 11-Jul-14 | 15-Jul-14 | 56 |
| LL2-8136 | LL2 - Chainlink Fencing / Gate @ Recycling | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 51 |
| LL2-8126 | LL2 - Doors & Hardware | 7 | 7 | 21-Jul-14 | 29-Jul-14 | 41 |
| LL2-8124 | LL2 - Flooring | 5 | 5 | 22-Jul-14 | 28-Jul-14 | 41 |
| LL2-8130 | LL2 - Substantially Complete | 0 | 0 | | 29-Jul-14 | 41 |
| LL2-8132 | LL2 - Contractor Pre-Punchlist | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 44 |
| LL2-8134 | LL2 - Pre-Clean | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 41 |
| LL2-8208 | LL2 - Final Clean | 3 | 3 | 06-Aug-14 | 08-Aug-14 | 41 |
| LL2-8210 | LL2 - Owner Walk / Create Punchlist | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 41 |
| LL2-8212 | LL2 - Final Punchlist | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 41 |
| LL2-8214 | LL2 - Floor Complete | 0 | 0 | | 18-Aug-14 | 41 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1U-8102 | Above Ceiling GWB | 5 | 5 | 10-Feb-14 A | 24-Mar-14 | 20 |
| LL1-Z2U-8102 | Above Ceiling GWB | 5 | 5 | 10-Feb-14 A | 24-Mar-14 | 45 |
| LL1-Z3U-8102 | Above Ceiling GWB | 5 | 5 | 10-Feb-14 A | 24-Mar-14 | 50 |
| L1BU-8102 | Above Ceiling GWB | 5 | 5 | 25-Apr-14 | 01-May-14 | 12 |
| L1LU-8102 | Above Ceiling GWB | 5 | 5 | 30-Apr-14 | 06-May-14 | 9 |
| L1KU-8102 | Above Ceiling GWB | 2 | 2 | 01-May-14 | 02-May-14 | 11 |
| LL1-8100 | Insulation | 5 | 5 | 03-Jun-14 | 09-Jun-14 | 8 |
| LL1-8102 | GWB Hang | 5 | 5 | 10-Jun-14 | 16-Jun-14 | 8 |
| LL1-Z2-8100 | Insulation | 5 | 5 | 10-Jun-14 | 16-Jun-14 | 8 |
| L1B-8100 | Insulation | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 12 |
| L1K-8100 | Insulation | 5 | 5 | 12-Jun-14 | 18-Jun-14 | 11 |
| L1L-8100 | Insulation | 5 | 5 | 16-Jun-14 | 20-Jun-14 | 9 |
| LL1-8215 | GWB Tape | 7 | 7 | 17-Jun-14 | 25-Jun-14 | 8 |
| LL1-Z2-8102 | GWB Hang | 5 | 5 | 17-Jun-14 | 23-Jun-14 | 13 |

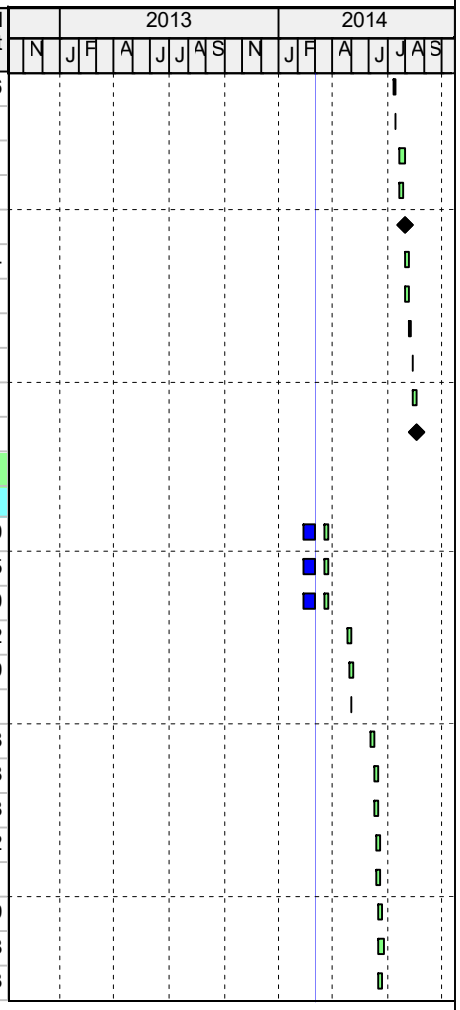



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8100 | Insulation | 5 | 5 | 17-Jun-14 | 23-Jun-14 | 8 |
| L1B-8102 | GWB Hang | 5 | 5 | 18-Jun-14 | 24-Jun-14 | 12 |
| L1K-8102 | GWB Hang | 5 | 5 | 19-Jun-14 | 25-Jun-14 | 11 |
| L1L-8102 | GWB Hang | 5 | 5 | 23-Jun-14 | 27-Jun-14 | 9 |
| LL1-Z2-8215 | GWB Tape | 7 | 7 | 24-Jun-14 | 02-Jul-14 | 13 |
| LL1-Z3-8102 | GWB Hang | 5 | 5 | 24-Jun-14 | 30-Jun-14 | 8 |
| L1B-8215 | GWB Tape | 7 | 7 | 25-Jun-14 | 03-Jul-14 | 12 |
| LL1-8104 | Prime Paint | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 8 |
| L1K-8215 | GWB Tape | 7 | 7 | 26-Jun-14 | 07-Jul-14 | 11 |
| L1L-8215 | GWB Tape | 7 | 7 | 30-Jun-14 | 09-Jul-14 | 9 |
| LL1-Z3-8215 | GWB Tape | 7 | 7 | 01-Jul-14 | 10-Jul-14 | 8 |
| LL1-8114 | T Bar Grid Ceiling | 3 | 3 | 03-Jul-14 | 08-Jul-14 | 70 |
| LL1-Z2-8104 | Prime Paint | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 13 |
| L1B-8104 | Prime Paint | 5 | 5 | 07-Jul-14 | 11-Jul-14 | 12 |
| L1K-8104 | Prime Paint | 5 | 5 | 08-Jul-14 | 14-Jul-14 | 11 |
| L1L-8104 | Prime Paint | 5 | 5 | 10-Jul-14 | 16-Jul-14 | 9 |
| LL1-8116 | Finish Carpentry / Millwork | 10 | 10 | 11-Jul-14 | 24-Jul-14 | 8 |
| LL1-Z2-8114 | T Bar Grid Ceiling | 3 | 3 | 11-Jul-14 | 15-Jul-14 | 65 |
| LL1-Z3-8104 | Prime Paint | 5 | 5 | 11-Jul-14 | 17-Jul-14 | 8 |
| L1B-8114 | T Bar Grid Ceiling | 3 | 3 | 14-Jul-14 | 16-Jul-14 | 64 |
| L1K-8114 | T Bar Grid Ceiling | 3 | 3 | 15-Jul-14 | 17-Jul-14 | 63 |
| L1L-8114 | T Bar Grid Ceiling | 3 | 3 | 17-Jul-14 | 21-Jul-14 | 61 |
| LL1-Z2-8116 | Finish Carpentry / Millwork | 10 | 10 | 18-Jul-14 | 31-Jul-14 | 13 |
| LL1-Z3-8114 | T Bar Grid Ceiling | 3 | 3 | 18-Jul-14 | 22-Jul-14 | 60 |
| L1B-8116 | Finish Carpentry / Millwork | 10 | 10 | 21-Jul-14 | 01-Aug-14 | 12 |
| L1K-8116 | Finish Carpentry / Millwork | 10 | 10 | 22-Jul-14 | 04-Aug-14 | 11 |
| L1L-8116 | Finish Carpentry / Millwork | 10 | 10 | 24-Jul-14 | 06-Aug-14 | 9 |

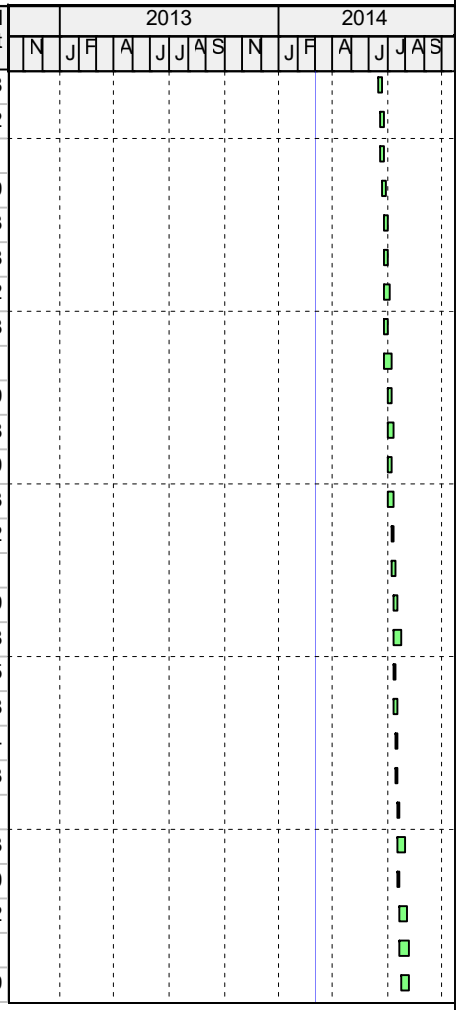



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8116 | Finish Carpentry / Millwork | 10 | 10 | 25-Jul-14 | 07-Aug-14 | 8 |
| LL1-8124 | Flooring | 5 | 5 | 01-Aug-14 | 07-Aug-14 | 8 |
| LL1-8126 | Doors & Hardware | 3 | 3 | 08-Aug-14 | 12-Aug-14 | 8 |
| LL1-8140 | Acoustical Ceiling Tile | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 46 |
| LL1-Z2-8124 | Flooring | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 13 |
| L1B-8124 | Flooring | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 12 |
| L1K-8124 | Flooring | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 11 |
| LL1-8106 | Wallcoverings | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 8 |
| L1L-8124 | Flooring | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 9 |
| LL1-Z2-8126 | Doors & Hardware | 3 | 3 | 15-Aug-14 | 19-Aug-14 | 13 |
| LL1-Z2-8140 | Acoustical Ceiling Tile | 2 | 2 | 15-Aug-14 | 18-Aug-14 | 41 |
| LL1-Z3-8124 | Flooring | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 8 |
| L1B-8126 | Doors & Hardware | 3 | 3 | 18-Aug-14 | 20-Aug-14 | 12 |
| L1B-8140 | Acoustical Ceiling Tile | 2 | 2 | 18-Aug-14 | 19-Aug-14 | 40 |
| L1K-8126 | Doors & Hardware | 3 | 3 | 19-Aug-14 | 21-Aug-14 | 11 |
| L1K-8140 | Acoustical Ceiling Tile | 2 | 2 | 19-Aug-14 | 20-Aug-14 | 39 |
| LL1-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 35 |
| LL1-8118 | Elec & Specialties Trim / Finish | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 35 |
| LL1-Z2-8106 | Wallcoverings | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 13 |
| L1B-8106 | Wallcoverings | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 12 |
| L1L-8126 | Doors & Hardware | 3 | 3 | 21-Aug-14 | 25-Aug-14 | 9 |
| L1L-8140 | Acoustical Ceiling Tile | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 37 |
| LL1-Z3-8126 | Doors & Hardware | 3 | 3 | 22-Aug-14 | 26-Aug-14 | 8 |
| LL1-Z3-8140 | Acoustical Ceiling Tile | 2 | 2 | 22-Aug-14 | 25-Aug-14 | 36 |
| L1K-8106 | Wallcoverings | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 11 |
| L1L-8106 | Wallcoverings | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 9 |
| LL1-8134 | Pre-Clean | 3 | 3 | 27-Aug-14 | 29-Aug-14 | 18 |

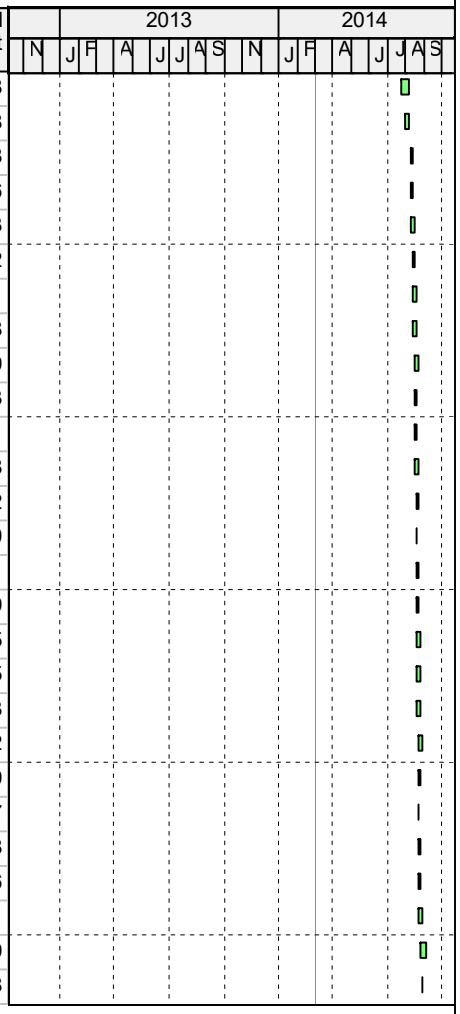



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 30 |
| LL1-Z2-8118 | Elec & Specialties Trim / Finish | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 30 |
| LL1-Z3-8106 | Wallcoverings | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 8 |
| L1B-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 29 |
| L1B-8118 | Elec & Specialties Trim / Finish | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 29 |
| L1K-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 28 |
| L1K-8118 | Elec & Specialties Trim / Finish | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 28 |
| LL1-8132 | Contractor Pre-Punchlist | 5 | 5 | 02-Sep-14 | 08-Sep-14 | 18 |
| L1L-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 26 |
| L1L-8118 | Elec & Specialties Trim / Finish | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 26 |
| LL1-Z2-8134 | Pre-Clean | 3 | 3 | 04-Sep-14 | 08-Sep-14 | 13 |
| LL1-Z3-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 25 |
| LL1-Z3-8118 | Elec & Specialties Trim / Finish | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 25 |
| L1B-8134 | Pre-Clean | 3 | 3 | 05-Sep-14 | 09-Sep-14 | 12 |
| L1K-8134 | Pre-Clean | 3 | 3 | 08-Sep-14 | 10-Sep-14 | 11 |
| LL1-Z2-8132 | Contractor Pre-Punchlist | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 13 |
| L1B-8132 | Contractor Pre-Punchlist | 5 | 5 | 10-Sep-14 | 16-Sep-14 | 12 |
| L1L-8134 | Pre-Clean | 3 | 3 | 10-Sep-14 | 12-Sep-14 | 9 |
| LL1-Z3-8134 | Pre-Clean | 3 | 3 | 11-Sep-14 | 15-Sep-14 | 8 |
| L1K-8132 | Contractor Pre-Punchlist | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 11 |
| L1L-8132 | Contractor Pre-Punchlist | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 9 |
| LL1-Z3-8132 | Contractor Pre-Punchlist | 5 | 5 | 16-Sep-14 | 22-Sep-14 | 8 |
| **Corridors / Common / Public Areas** | | | | | | |
| LL1-8200 | First Coat Finish Paint | 5 | 5 | 25-Jul-14 | 31-Jul-14 | 8 |
| LL1-Z2-8200 | First Coat Finish Paint | 5 | 5 | 01-Aug-14 | 07-Aug-14 | 13 |
| L1B-8200 | First Coat Finish Paint | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 12 |
| L1K-8200 | First Coat Finish Paint | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 11 |

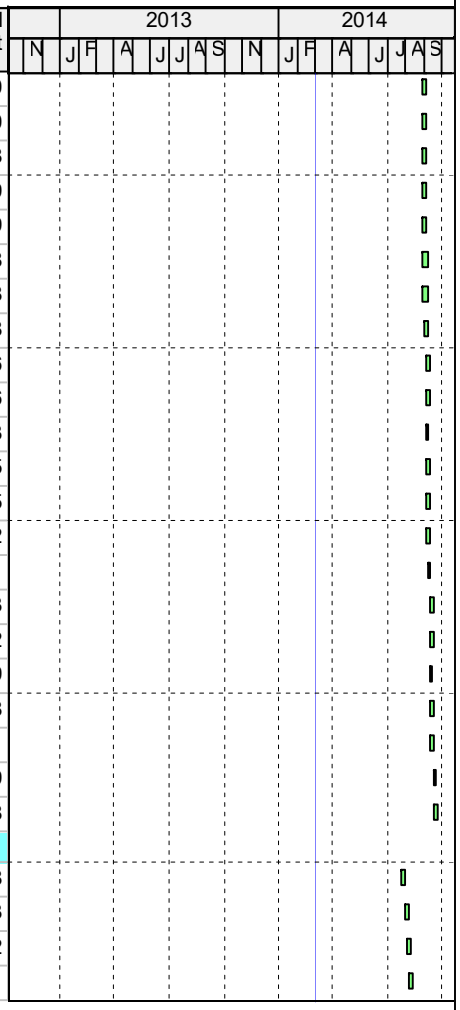



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8200 | First Coat Finish Paint | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 9 |
| LL1-Z3-8200 | First Coat Finish Paint | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 8 |
| LL1-8201 | Final Coat Finish Paint | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 8 |
| LL1-8204 | Mech Trim / Finish | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 8 |
| LL1-Z2-8201 | Final Coat Finish Paint | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 13 |
| L1B-8201 | Final Coat Finish Paint | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 12 |
| L1K-8201 | Final Coat Finish Paint | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 11 |
| L1L-8201 | Final Coat Finish Paint | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 9 |
| LL1-Z2-8204 | Mech Trim / Finish | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 13 |
| LL1-Z3-8201 | Final Coat Finish Paint | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 8 |
| L1B-8204 | Mech Trim / Finish | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 12 |
| L1K-8204 | Mech Trim / Finish | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 11 |
| L1L-8204 | Mech Trim / Finish | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 9 |
| LL1-Z3-8204 | Mech Trim / Finish | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 8 |
| LL1-8210 | Owner Walk / Create Punchlist | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 18 |
| LL1-8212 | Final Punchlist | 5 | 5 | 10-Sep-14 | 16-Sep-14 | 18 |
| LL1-Z2-8210 | Owner Walk / Create Punchlist | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 13 |
| LL1-8208 | Final Clean | 3 | 3 | 17-Sep-14 | 19-Sep-14 | 18 |
| LL1-Z2-8212 | Final Punchlist | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 13 |
| L1B-8210 | Owner Walk / Create Punchlist | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 12 |
| L1B-8212 | Final Punchlist | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 12 |
| L1K-8210 | Owner Walk / Create Punchlist | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 11 |
| L1K-8212 | Final Punchlist | 5 | 5 | 19-Sep-14 | 25-Sep-14 | 11 |
| LL1-8214 | Floor Complete | 0 | 0 | | 19-Sep-14 | 18 |
| L1L-8210 | Owner Walk / Create Punchlist | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 9 |
| LL1-Z3-8210 | Owner Walk / Create Punchlist | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 8 |
| L1L-8212 | Final Punchlist | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 9 |

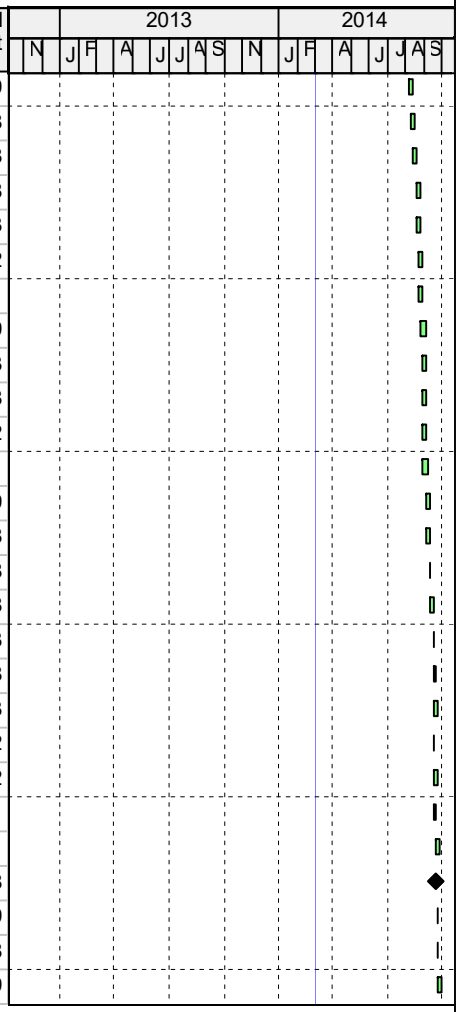



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-8208 | Final Clean | 3 | 3 | 24-Sep-14 | 26-Sep-14 | 13 |
| LL1-Z3-8212 | Final Punchlist | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 8 |
| L1B-8208 | Final Clean | 3 | 3 | 25-Sep-14 | 29-Sep-14 | 12 |
| L1K-8208 | Final Clean | 3 | 3 | 26-Sep-14 | 30-Sep-14 | 11 |
| LL1-Z2-8214 | Floor Complete | 0 | 0 | | 26-Sep-14 | 13 |
| L1B-8214 | Floor Complete | 0 | 0 | | 29-Sep-14 | 12 |
| L1L-8208 | Final Clean | 3 | 3 | 30-Sep-14 | 02-Oct-14 | 9 |
| L1K-8214 | Floor Complete | 0 | 0 | | 30-Sep-14 | 11 |
| LL1-Z3-8208 | Final Clean | 3 | 3 | 01-Oct-14 | 03-Oct-14 | 8 |
| L1L-8214 | Floor Complete | 0 | 0 | | 02-Oct-14 | 9 |
| LL1-Z3-8214 | Floor Complete | 0 | 0 | | 03-Oct-14 | 8 |
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8100 | L2 - Insulation | 5 | 5 | 04-Jun-14 | 10-Jun-14 | 8 |
| L02-8102 | L2 - GWB Hang / Tape / Finish - (Including Common / | 20 | 20 | 11-Jun-14 | 09-Jul-14 | 8 |
| L02-8104 | L2 - Int Painting | 10 | 10 | 07-Jul-14 | 18-Jul-14 | 8 |
| L02-8106 | L2 - Wallcoverings | 6 | 6 | 09-Jul-14 | 16-Jul-14 | 20 |
| L02-8116 | L2 - Finish Carpentry / Millwork | 5 | 5 | 14-Jul-14 | 18-Jul-14 | 13 |
| L02-8120 | L2 - Ceramic Tile / Counter Tops | 8 | 8 | 16-Jul-14 | 25-Jul-14 | 13 |
| L02-8122 | L2 - Plumbing Trim / Finish | 8 | 8 | 18-Jul-14 | 29-Jul-14 | 15 |
| L02-8108 | L2 - Elec Trim / Finish | 10 | 10 | 21-Jul-14 | 01-Aug-14 | 8 |
| L02-8110 | L2 - HVAC Trim / Finish | 10 | 10 | 21-Jul-14 | 01-Aug-14 | 8 |
| L02-8112 | L2 - Fire Sprinkler Trim / Finish | 8 | 8 | 21-Jul-14 | 30-Jul-14 | 10 |
| L02-8118 | L2 - Elec Specialties Trim / Finish | 10 | 10 | 21-Jul-14 | 01-Aug-14 | 8 |
| L02-8136 | L2 - Lockers / Benches @ Locker Rooms | 5 | 5 | 21-Jul-14 | 25-Jul-14 | 19 |
| L02-8128 | L2 - Bath Specialties | 2 | 2 | 30-Jul-14 | 31-Jul-14 | 15 |
| L02-8124 | L2 - Flooring | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 8 |

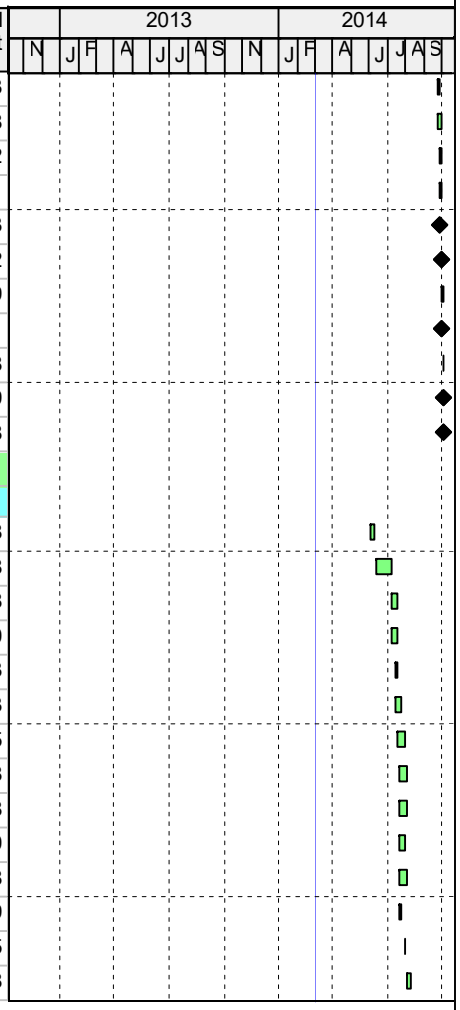



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8126 | L2 - Doors & Hardware | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 8 |
| L02-8130 | L2 - Admin / Employee Rooms Substantially Complet | 0 | 0 | | 11-Aug-14 | 8 |
| L02-8132 | L2 - Contractor Pre-Punchlist | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 35 |
| L02-8134 | L2 - Pre-Clean | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 30 |
| **Corridors** | | | | | | |
| L02-8200 | L2 - Final Paint @ Common / Public Areas | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 8 |
| L02-8114 | L2 - Signage | 3 | 3 | 19-Aug-14 | 21-Aug-14 | 27 |
| L02-8202 | L2 - Elec Trim / Finish @ Common / Public Areas | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 8 |
| L02-8204 | L2 - Mech Trim / Finish @ Common / Public Areas | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 8 |
| L02-8206 | L2 - Flooring @ Corridors | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 20 |
| L02-8208 | L2 - Final Clean | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 20 |
| L02-8210 | L2 - Owner Walk / Create Punchlist | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 20 |
| L02-8212 | L2 - Final Punchlist | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 20 |
| L02-8214 | L2 - Floor Complete | 0 | 0 | | 17-Sep-14 | 20 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L05-8102S | Stock GWB | 2 | 2 | 26-Mar-14 | 27-Mar-14 | 14 |
| L03-8102S | Stock GWB | 2 | 2 | 01-Apr-14 | 02-Apr-14 | 0 |
| L04-8102S | Stock GWB | 2 | 2 | 01-Apr-14 | 02-Apr-14 | 5 |
| L06-8102S | Stock GWB | 2 | 2 | 01-Apr-14 | 02-Apr-14 | 15 |
| L03-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 03-Apr-14 | 11-Apr-14 | 0 |
| L07-8102S | Stock GWB | 2 | 2 | 08-Apr-14 | 09-Apr-14 | 15 |
| L04-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 10-Apr-14 | 18-Apr-14 | 0 |
| L08-8102S | Stock GWB | 2 | 2 | 15-Apr-14 | 16-Apr-14 | 15 |
| L05-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 17-Apr-14 | 25-Apr-14 | 0 |
| L03-8104 | Primer Paint Coat | 2 | 2 | 22-Apr-14 | 23-Apr-14 | 80 |

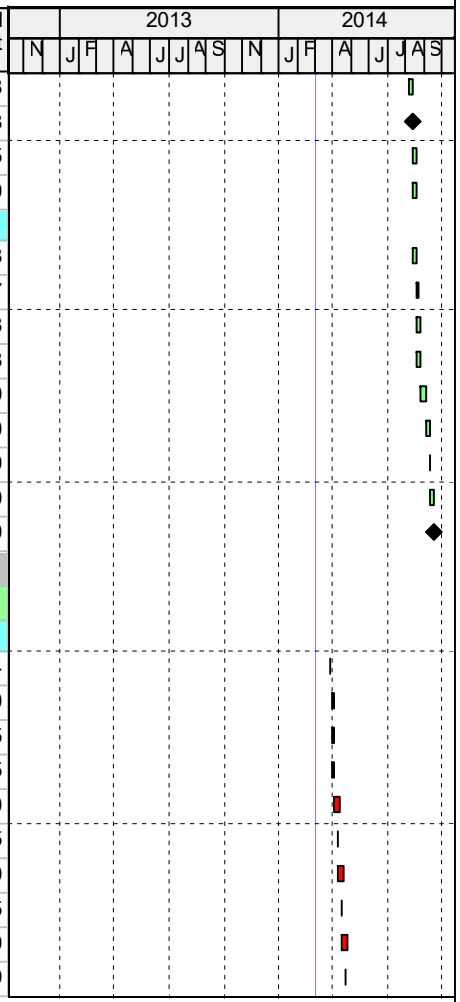


Actual Work | Remaining Work | Critical Remai... | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8102S | Stock GWB | 2 | 2 | 22-Apr-14 | 23-Apr-14 | 15 |
| L03-8120 | Install Casework/Countertops | 5 | 5 | 24-Apr-14 | 30-Apr-14 | 80 |
| L06-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 24-Apr-14 | 02-May-14 | 0 |
| L03-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 29-Apr-14 | 05-May-14 | 80 |
| L04-8104 | Primer Paint Coat | 2 | 2 | 29-Apr-14 | 30-Apr-14 | 75 |
| L10-8102S | Stock GWB | 2 | 2 | 29-Apr-14 | 30-Apr-14 | 15 |
| L03-8116 | Install Wood Base | 3 | 3 | 01-May-14 | 05-May-14 | 80 |
| L04-8120 | Install Casework/Countertops | 5 | 5 | 01-May-14 | 07-May-14 | 75 |
| L07-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 01-May-14 | 09-May-14 | 0 |
| L03-8128 | Install Tub Glazing | 4 | 4 | 02-May-14 | 07-May-14 | 80 |
| L03-8105 | First Coat Finish Paint | 5 | 5 | 06-May-14 | 12-May-14 | 80 |
| L04-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 06-May-14 | 12-May-14 | 75 |
| L05-8104 | Primer Paint Coat | 2 | 2 | 06-May-14 | 07-May-14 | 70 |
| L11-8102S | Stock GWB | 2 | 2 | 06-May-14 | 07-May-14 | 15 |
| L03-8124 | Flooring @ Guest Rooms | 5 | 5 | 08-May-14 | 14-May-14 | 80 |
| L04-8116 | Install Wood Base | 3 | 3 | 08-May-14 | 12-May-14 | 75 |
| L05-8120 | Install Casework/Countertops | 5 | 5 | 08-May-14 | 14-May-14 | 70 |
| L08-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 08-May-14 | 16-May-14 | 0 |
| L04-8128 | Install Tub Glazing | 4 | 4 | 09-May-14 | 14-May-14 | 75 |
| L03-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 13-May-14 | 15-May-14 | 80 |
| L04-8105 | First Coat Finish Paint | 5 | 5 | 13-May-14 | 19-May-14 | 75 |
| L05-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 13-May-14 | 19-May-14 | 70 |
| L06-8104 | Primer Paint Coat | 2 | 2 | 13-May-14 | 14-May-14 | 65 |
| L04-8124 | Flooring @ Guest Rooms | 5 | 5 | 15-May-14 | 21-May-14 | 75 |
| L05-8116 | Install Wood Base | 3 | 3 | 15-May-14 | 19-May-14 | 70 |
| L06-8120 | Install Casework/Countertops | 5 | 5 | 15-May-14 | 21-May-14 | 65 |
| L09-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 15-May-14 | 23-May-14 | 0 |

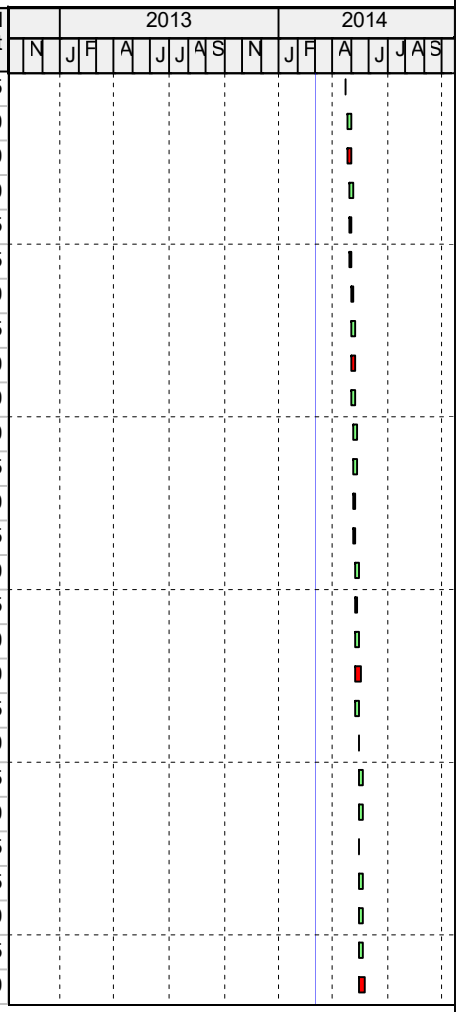



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8107 | Final Coat Finish Paint | 5 | 5 | 16-May-14 | 22-May-14 | 80 |
| L05-8128 | Install Tub Glazing | 4 | 4 | 16-May-14 | 21-May-14 | 70 |
| L04-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 20-May-14 | 22-May-14 | 75 |
| L05-8105 | First Coat Finish Paint | 5 | 5 | 20-May-14 | 27-May-14 | 70 |
| L06-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 20-May-14 | 27-May-14 | 65 |
| L07-8104 | Primer Paint Coat | 2 | 2 | 20-May-14 | 21-May-14 | 60 |
| L12-8102S | Stock GWB | 2 | 2 | 20-May-14 | 21-May-14 | 25 |
| L03-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 21-May-14 | 28-May-14 | 84 |
| L03-8108 | Elec Trim / Finish | 5 | 5 | 21-May-14 | 28-May-14 | 84 |
| L03-8110 | HVAC Trim / Finish | 5 | 5 | 21-May-14 | 28-May-14 | 84 |
| L03-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 21-May-14 | 28-May-14 | 84 |
| L05-8124 | Flooring @ Guest Rooms | 5 | 5 | 22-May-14 | 29-May-14 | 70 |
| L06-8116 | Install Wood Base | 3 | 3 | 22-May-14 | 27-May-14 | 65 |
| L07-8120 | Install Casework/Countertops | 5 | 5 | 22-May-14 | 29-May-14 | 60 |
| L10-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 22-May-14 | 02-Jun-14 | 0 |
| L03-8126 | Doors & Hardware | 5 | 5 | 23-May-14 | 30-May-14 | 80 |
| L03-8118 | Elec Specialties Trim / Finish | 4 | 4 | 23-May-14 | 29-May-14 | 83 |
| L04-8107 | Final Coat Finish Paint | 5 | 5 | 23-May-14 | 30-May-14 | 75 |
| L06-8128 | Install Tub Glazing | 4 | 4 | 23-May-14 | 29-May-14 | 65 |
| L05-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 28-May-14 | 30-May-14 | 70 |
| L06-8105 | First Coat Finish Paint | 5 | 5 | 28-May-14 | 03-Jun-14 | 65 |
| L07-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 28-May-14 | 03-Jun-14 | 60 |
| L08-8104 | Primer Paint Coat | 2 | 2 | 28-May-14 | 29-May-14 | 55 |
| L14-8102S | Stock GWB | 2 | 2 | 28-May-14 | 29-May-14 | 25 |
| L04-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 29-May-14 | 04-Jun-14 | 79 |
| L04-8108 | Elec Trim / Finish | 5 | 5 | 29-May-14 | 04-Jun-14 | 79 |
| L04-8110 | HVAC Trim / Finish | 5 | 5 | 29-May-14 | 04-Jun-14 | 79 |

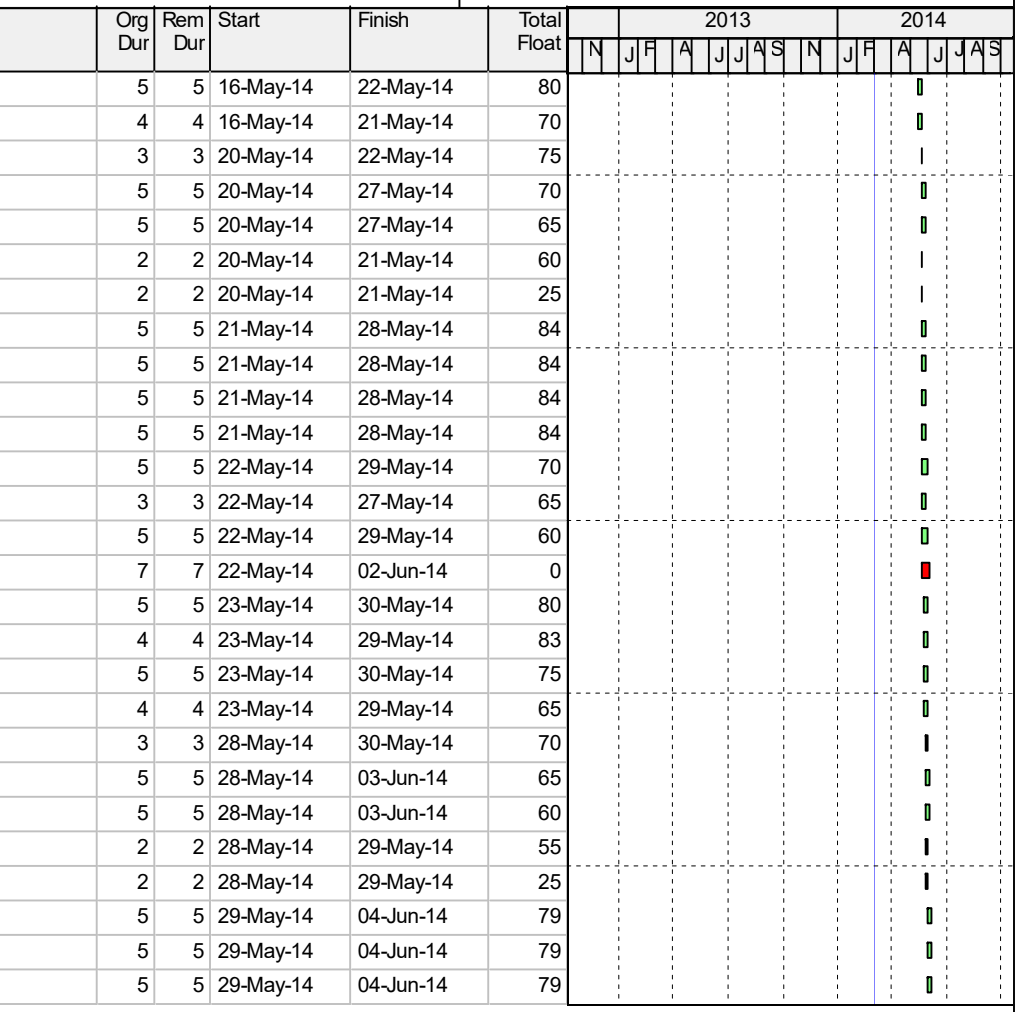



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 29-May-14 | 04-Jun-14 | 79 |
| L03-8114 | Signage (By Owner) | 3 | 3 | 30-May-14 | 03-Jun-14 | 80 |
| L06-8124 | Flooring @ Guest Rooms | 5 | 5 | 30-May-14 | 05-Jun-14 | 65 |
| L07-8116 | Install Wood Base | 3 | 3 | 30-May-14 | 03-Jun-14 | 60 |
| L08-8120 | Install Casework/Countertops | 5 | 5 | 30-May-14 | 05-Jun-14 | 55 |
| L11-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 30-May-14 | 09-Jun-14 | 0 |
| L04-8126 | Doors & Hardware | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 75 |
| L04-8118 | Elec Specialties Trim / Finish | 4 | 4 | 02-Jun-14 | 05-Jun-14 | 78 |
| L05-8107 | Final Coat Finish Paint | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 70 |
| L07-8128 | Install Tub Glazing | 4 | 4 | 02-Jun-14 | 05-Jun-14 | 60 |
| L03-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 03-Jun-14 | 80 |
| L03-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 04-Jun-14 | 10-Jun-14 | 83 |
| L03-8134 | Pre-Clean Guestrooms | 5 | 5 | 04-Jun-14 | 10-Jun-14 | 80 |
| L06-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 04-Jun-14 | 06-Jun-14 | 65 |
| L07-8105 | First Coat Finish Paint | 5 | 5 | 04-Jun-14 | 10-Jun-14 | 60 |
| L08-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 04-Jun-14 | 10-Jun-14 | 55 |
| L09-8104 | Primer Paint Coat | 2 | 2 | 04-Jun-14 | 05-Jun-14 | 50 |
| L15-8102S | Stock GWB | 2 | 2 | 04-Jun-14 | 05-Jun-14 | 25 |
| L05-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 74 |
| L05-8108 | Elec Trim / Finish | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 74 |
| L05-8110 | HVAC Trim / Finish | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 74 |
| L05-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 74 |
| L04-8114 | Signage (By Owner) | 3 | 3 | 06-Jun-14 | 10-Jun-14 | 75 |
| L07-8124 | Flooring @ Guest Rooms | 5 | 5 | 06-Jun-14 | 12-Jun-14 | 60 |
| L08-8116 | Install Wood Base | 3 | 3 | 06-Jun-14 | 10-Jun-14 | 55 |
| L09-8120 | Install Casework/Countertops | 5 | 5 | 06-Jun-14 | 12-Jun-14 | 50 |
| L12-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 06-Jun-14 | 16-Jun-14 | 15 |

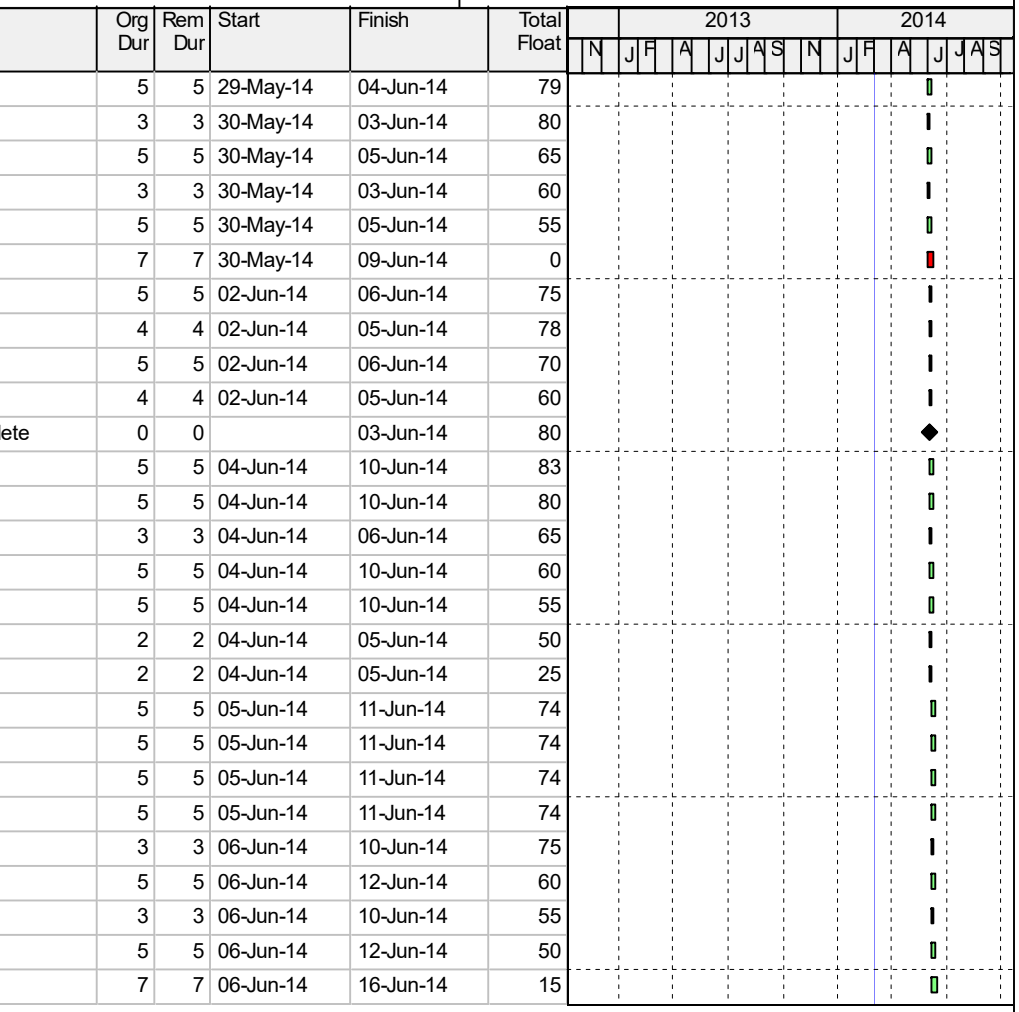



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8126 | Doors & Hardware | 5 | 5 | 09-Jun-14 | 13-Jun-14 | 70 |
| L05-8118 | Elec Specialties Trim / Finish | 4 | 4 | 09-Jun-14 | 12-Jun-14 | 73 |
| L06-8107 | Final Coat Finish Paint | 5 | 5 | 09-Jun-14 | 13-Jun-14 | 65 |
| L08-8128 | Install Tub Glazing | 4 | 4 | 09-Jun-14 | 12-Jun-14 | 55 |
| L04-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 10-Jun-14 | 75 |
| L04-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 78 |
| L04-8134 | Pre-Clean Guestrooms | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 75 |
| L07-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 11-Jun-14 | 13-Jun-14 | 60 |
| L08-8105 | First Coat Finish Paint | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 55 |
| L09-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 50 |
| L10-8104 | Primer Paint Coat | 2 | 2 | 11-Jun-14 | 12-Jun-14 | 45 |
| L16-8102S | Stock GWB | 2 | 2 | 11-Jun-14 | 12-Jun-14 | 25 |
| L06-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 12-Jun-14 | 18-Jun-14 | 69 |
| L06-8108 | Elec Trim / Finish | 5 | 5 | 12-Jun-14 | 18-Jun-14 | 69 |
| L06-8110 | HVAC Trim / Finish | 5 | 5 | 12-Jun-14 | 18-Jun-14 | 69 |
| L06-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 12-Jun-14 | 18-Jun-14 | 69 |
| L05-8114 | Signage (By Owner) | 3 | 3 | 13-Jun-14 | 17-Jun-14 | 70 |
| L08-8124 | Flooring @ Guest Rooms | 5 | 5 | 13-Jun-14 | 19-Jun-14 | 55 |
| L09-8116 | Install Wood Base | 3 | 3 | 13-Jun-14 | 17-Jun-14 | 50 |
| L10-8120 | Install Casework/Countertops | 5 | 5 | 13-Jun-14 | 19-Jun-14 | 45 |
| L14-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 13-Jun-14 | 23-Jun-14 | 15 |
| L06-8126 | Doors & Hardware | 5 | 5 | 16-Jun-14 | 20-Jun-14 | 65 |
| L06-8118 | Elec Specialties Trim / Finish | 4 | 4 | 16-Jun-14 | 19-Jun-14 | 68 |
| L07-8107 | Final Coat Finish Paint | 5 | 5 | 16-Jun-14 | 20-Jun-14 | 60 |
| L09-8128 | Install Tub Glazing | 4 | 4 | 16-Jun-14 | 19-Jun-14 | 50 |
| L17-8102S | Stock GWB | 2 | 2 | 17-Jun-14 | 18-Jun-14 | 26 |
| L05-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 17-Jun-14 | 70 |

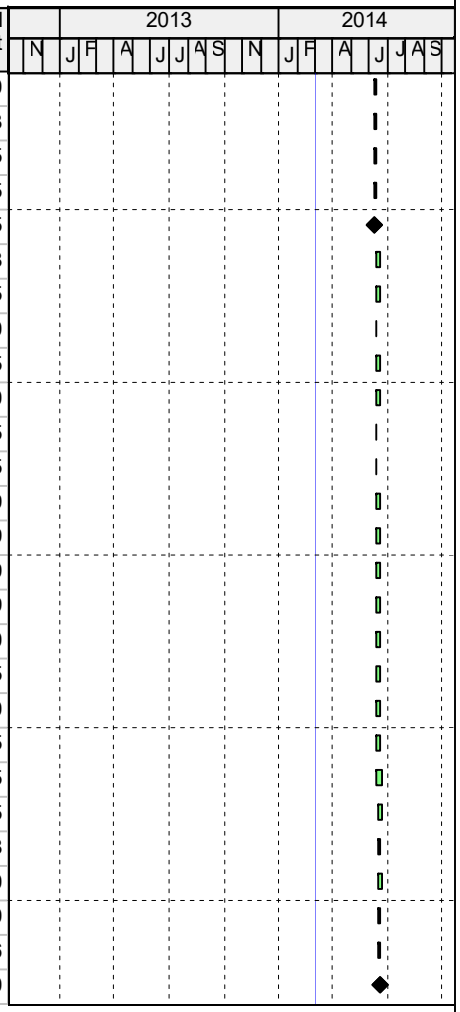



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 18-Jun-14 | 24-Jun-14 | 73 |
| L05-8134 | Pre-Clean Guestrooms | 5 | 5 | 18-Jun-14 | 24-Jun-14 | 70 |
| L08-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 18-Jun-14 | 20-Jun-14 | 55 |
| L09-8105 | First Coat Finish Paint | 5 | 5 | 18-Jun-14 | 24-Jun-14 | 50 |
| L10-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 18-Jun-14 | 24-Jun-14 | 45 |
| L11-8104 | Primer Paint Coat | 2 | 2 | 18-Jun-14 | 19-Jun-14 | 0 |
| L07-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 19-Jun-14 | 25-Jun-14 | 64 |
| L07-8108 | Elec Trim / Finish | 5 | 5 | 19-Jun-14 | 25-Jun-14 | 64 |
| L07-8110 | HVAC Trim / Finish | 5 | 5 | 19-Jun-14 | 25-Jun-14 | 64 |
| L07-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 19-Jun-14 | 25-Jun-14 | 64 |
| L06-8114 | Signage (By Owner) | 3 | 3 | 20-Jun-14 | 24-Jun-14 | 65 |
| L09-8124 | Flooring @ Guest Rooms | 5 | 5 | 20-Jun-14 | 26-Jun-14 | 50 |
| L10-8116 | Install Wood Base | 3 | 3 | 20-Jun-14 | 24-Jun-14 | 45 |
| L11-8120 | Install Casework/Countertops | 5 | 5 | 20-Jun-14 | 26-Jun-14 | 0 |
| L15-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 20-Jun-14 | 30-Jun-14 | 15 |
| L07-8126 | Doors & Hardware | 5 | 5 | 23-Jun-14 | 27-Jun-14 | 60 |
| L07-8118 | Elec Specialties Trim / Finish | 4 | 4 | 23-Jun-14 | 26-Jun-14 | 63 |
| L08-8107 | Final Coat Finish Paint | 5 | 5 | 23-Jun-14 | 27-Jun-14 | 55 |
| L10-8128 | Install Tub Glazing | 4 | 4 | 23-Jun-14 | 26-Jun-14 | 45 |
| L06-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 24-Jun-14 | 65 |
| L06-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 25-Jun-14 | 01-Jul-14 | 68 |
| L06-8134 | Pre-Clean Guestrooms | 5 | 5 | 25-Jun-14 | 01-Jul-14 | 65 |
| L09-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 25-Jun-14 | 27-Jun-14 | 50 |
| L10-8105 | First Coat Finish Paint | 5 | 5 | 25-Jun-14 | 01-Jul-14 | 45 |
| L11-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 25-Jun-14 | 01-Jul-14 | 0 |
| L12-8104 | Primer Paint Coat | 2 | 2 | 25-Jun-14 | 26-Jun-14 | 35 |
| L08-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 59 |

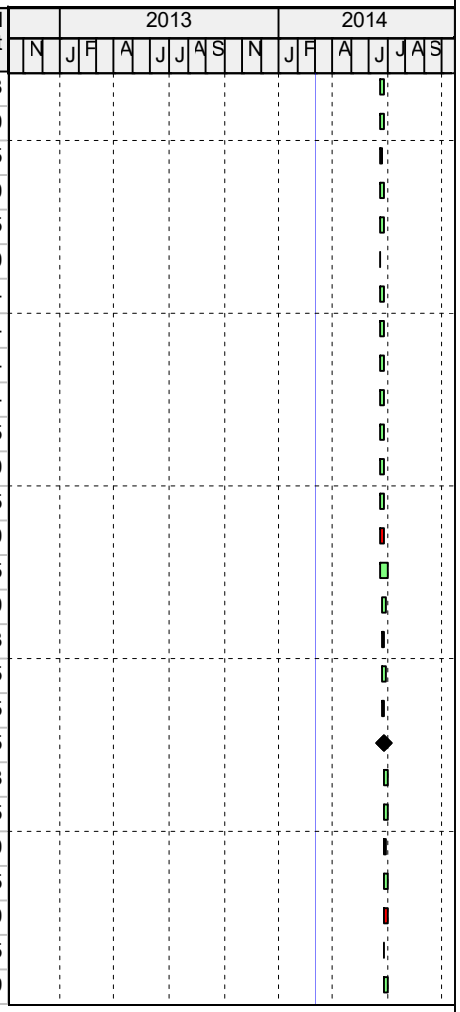



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8108 | Elec Trim / Finish | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 59 |
| L08-8110 | HVAC Trim / Finish | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 59 |
| L08-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 59 |
| L07-8114 | Signage (By Owner) | 3 | 3 | 27-Jun-14 | 01-Jul-14 | 60 |
| L10-8124 | Flooring @ Guest Rooms | 5 | 5 | 27-Jun-14 | 03-Jul-14 | 45 |
| L11-8116 | Install Wood Base | 3 | 3 | 27-Jun-14 | 01-Jul-14 | 0 |
| L12-8120 | Install Casework/Countertops | 5 | 5 | 27-Jun-14 | 03-Jul-14 | 35 |
| L16-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 27-Jun-14 | 08-Jul-14 | 15 |
| L08-8126 | Doors & Hardware | 5 | 5 | 30-Jun-14 | 07-Jul-14 | 55 |
| L08-8118 | Elec Specialties Trim / Finish | 4 | 4 | 30-Jun-14 | 03-Jul-14 | 58 |
| L09-8107 | Final Coat Finish Paint | 5 | 5 | 30-Jun-14 | 07-Jul-14 | 50 |
| L11-8128 | Install Tub Glazing | 4 | 4 | 30-Jun-14 | 03-Jul-14 | 0 |
| L07-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 |  | 01-Jul-14 | 60 |
| L07-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 02-Jul-14 | 09-Jul-14 | 63 |
| L07-8134 | Pre-Clean Guestrooms | 5 | 5 | 02-Jul-14 | 09-Jul-14 | 60 |
| L10-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 02-Jul-14 | 07-Jul-14 | 45 |
| L11-8105 | First Coat Finish Paint | 5 | 5 | 02-Jul-14 | 09-Jul-14 | 0 |
| L12-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 02-Jul-14 | 09-Jul-14 | 35 |
| L14-8104 | Primer Paint Coat | 2 | 2 | 02-Jul-14 | 03-Jul-14 | 30 |
| L09-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 54 |
| L09-8108 | Elec Trim / Finish | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 54 |
| L09-8110 | HVAC Trim / Finish | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 54 |
| L09-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 54 |
| L08-8114 | Signage (By Owner) | 3 | 3 | 07-Jul-14 | 09-Jul-14 | 55 |
| L11-8124 | Flooring @ Guest Rooms | 5 | 5 | 07-Jul-14 | 11-Jul-14 | 0 |
| L12-8116 | Install Wood Base | 3 | 3 | 07-Jul-14 | 09-Jul-14 | 35 |
| L14-8120 | Install Casework/Countertops | 5 | 5 | 07-Jul-14 | 11-Jul-14 | 30 |

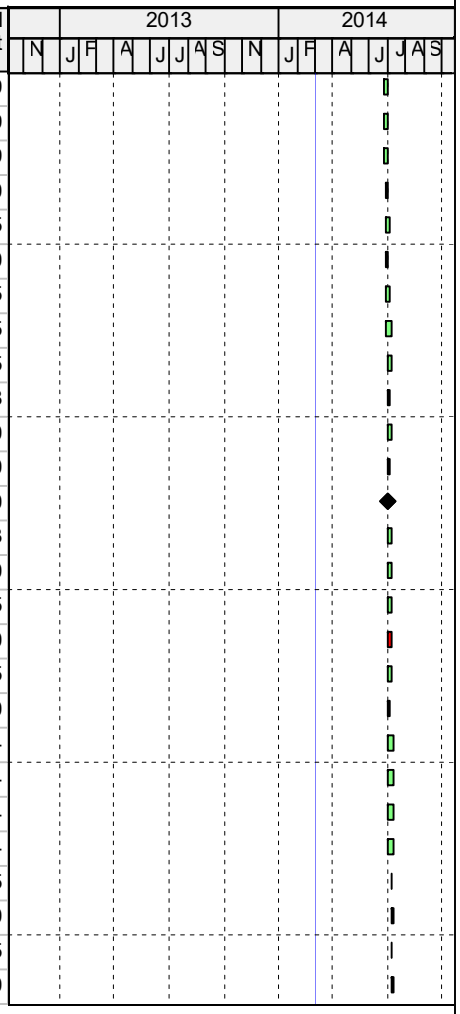



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 07-Jul-14 | 15-Jul-14 | 15 |
| L09-8126 | Doors & Hardware | 5 | 5 | 08-Jul-14 | 14-Jul-14 | 50 |
| L09-8118 | Elec Specialties Trim / Finish | 4 | 4 | 08-Jul-14 | 11-Jul-14 | 53 |
| L10-8107 | Final Coat Finish Paint | 5 | 5 | 08-Jul-14 | 14-Jul-14 | 45 |
| L12-8128 | Install Tub Glazing | 4 | 4 | 08-Jul-14 | 11-Jul-14 | 35 |
| L08-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 09-Jul-14 | 55 |
| L08-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 10-Jul-14 | 16-Jul-14 | 58 |
| L08-8134 | Pre-Clean Guestrooms | 5 | 5 | 10-Jul-14 | 16-Jul-14 | 55 |
| L11-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 10-Jul-14 | 14-Jul-14 | 0 |
| L12-8105 | First Coat Finish Paint | 5 | 5 | 10-Jul-14 | 16-Jul-14 | 35 |
| L14-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 10-Jul-14 | 16-Jul-14 | 30 |
| L15-8104 | Primer Paint Coat | 2 | 2 | 10-Jul-14 | 11-Jul-14 | 25 |
| L10-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 11-Jul-14 | 17-Jul-14 | 49 |
| L10-8108 | Elec Trim / Finish | 5 | 5 | 11-Jul-14 | 17-Jul-14 | 49 |
| L10-8110 | HVAC Trim / Finish | 5 | 5 | 11-Jul-14 | 17-Jul-14 | 49 |
| L10-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 11-Jul-14 | 17-Jul-14 | 49 |
| L09-8114 | Signage (By Owner) | 3 | 3 | 14-Jul-14 | 16-Jul-14 | 50 |
| L12-8124 | Flooring @ Guest Rooms | 5 | 5 | 14-Jul-14 | 18-Jul-14 | 35 |
| L14-8116 | Install Wood Base | 3 | 3 | 14-Jul-14 | 16-Jul-14 | 30 |
| L15-8120 | Install Casework/Countertops | 5 | 5 | 14-Jul-14 | 18-Jul-14 | 25 |
| L10-8126 | Doors & Hardware | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 45 |
| L10-8118 | Elec Specialties Trim / Finish | 4 | 4 | 15-Jul-14 | 18-Jul-14 | 48 |
| L11-8107 | Final Coat Finish Paint | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 0 |
| L14-8128 | Install Tub Glazing | 4 | 4 | 15-Jul-14 | 18-Jul-14 | 30 |
| L09-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 16-Jul-14 | 50 |
| L09-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 17-Jul-14 | 23-Jul-14 | 53 |
| L09-8134 | Pre-Clean Guestrooms | 5 | 5 | 17-Jul-14 | 23-Jul-14 | 50 |

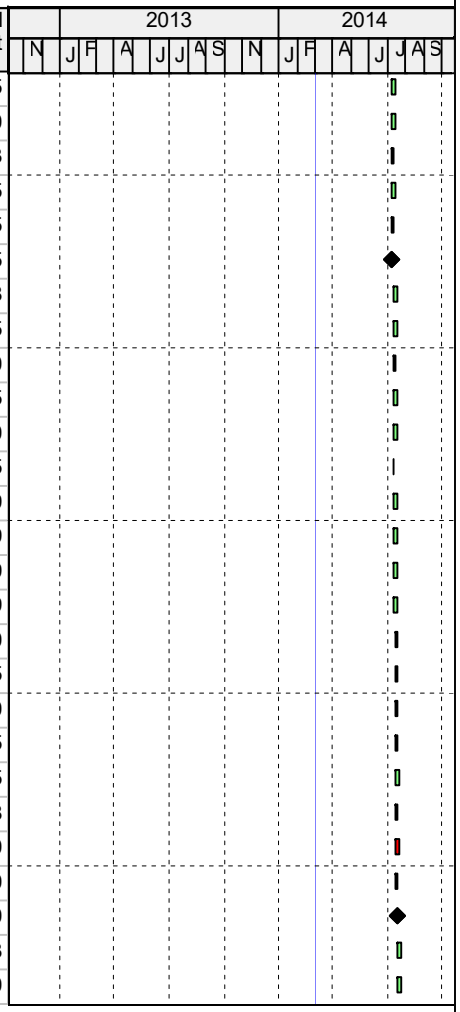



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 17-Jul-14 | 21-Jul-14 | 35 |
| L14-8105 | First Coat Finish Paint | 5 | 5 | 17-Jul-14 | 23-Jul-14 | 30 |
| L15-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 17-Jul-14 | 23-Jul-14 | 25 |
| L16-8104 | Primer Paint Coat | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 20 |
| L11-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 18-Jul-14 | 24-Jul-14 | 4 |
| L11-8108 | Elec Trim / Finish | 5 | 5 | 18-Jul-14 | 24-Jul-14 | 4 |
| L11-8110 | HVAC Trim / Finish | 5 | 5 | 18-Jul-14 | 24-Jul-14 | 4 |
| L11-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 18-Jul-14 | 24-Jul-14 | 4 |
| L10-8114 | Signage (By Owner) | 3 | 3 | 21-Jul-14 | 23-Jul-14 | 45 |
| L14-8124 | Flooring @ Guest Rooms | 5 | 5 | 21-Jul-14 | 25-Jul-14 | 30 |
| L15-8116 | Install Wood Base | 3 | 3 | 21-Jul-14 | 23-Jul-14 | 25 |
| L16-8120 | Install Casework/Countertops | 5 | 5 | 21-Jul-14 | 25-Jul-14 | 20 |
| L11-8126 | Doors & Hardware | 5 | 5 | 22-Jul-14 | 28-Jul-14 | 0 |
| L11-8118 | Elec Specialties Trim / Finish | 4 | 4 | 22-Jul-14 | 25-Jul-14 | 3 |
| L12-8107 | Final Coat Finish Paint | 5 | 5 | 22-Jul-14 | 28-Jul-14 | 35 |
| L15-8128 | Install Tub Glazing | 4 | 4 | 22-Jul-14 | 25-Jul-14 | 25 |
| L10-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 23-Jul-14 | 45 |
| L10-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 48 |
| L10-8134 | Pre-Clean Guestrooms | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 45 |
| L14-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 24-Jul-14 | 28-Jul-14 | 30 |
| L15-8105 | First Coat Finish Paint | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 25 |
| L16-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 20 |
| L17-8104 | Primer Paint Coat | 2 | 2 | 24-Jul-14 | 25-Jul-14 | 15 |
| L12-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 25-Jul-14 | 31-Jul-14 | 39 |
| L12-8108 | Elec Trim / Finish | 5 | 5 | 25-Jul-14 | 31-Jul-14 | 39 |
| L12-8110 | HVAC Trim / Finish | 5 | 5 | 25-Jul-14 | 31-Jul-14 | 39 |
| L12-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 25-Jul-14 | 31-Jul-14 | 39 |

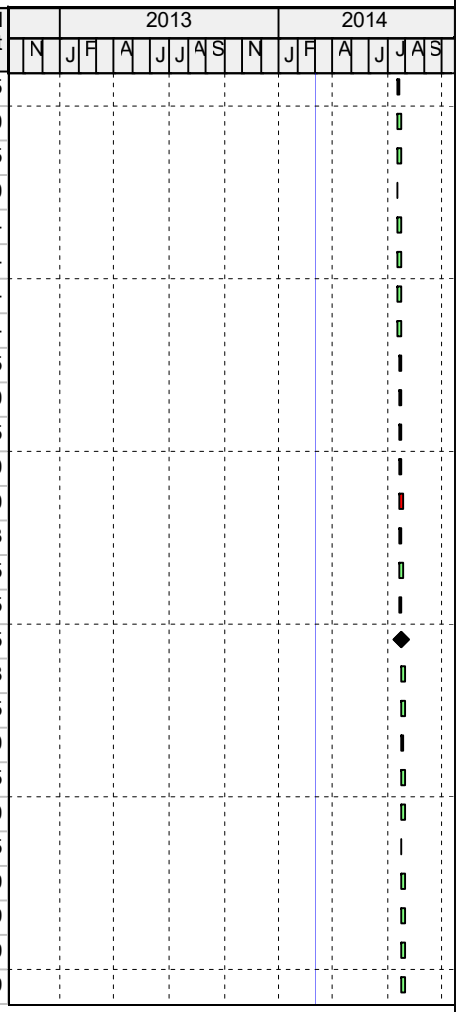



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8114 | Signage (By Owner) | 3 | 3 | 28-Jul-14 | 30-Jul-14 | 0 |
| L15-8124 | Flooring @ Guest Rooms | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 25 |
| L16-8116 | Install Wood Base | 3 | 3 | 28-Jul-14 | 30-Jul-14 | 20 |
| L17-8120 | Install Casework/Countertops | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 15 |
| L12-8126 | Doors & Hardware | 5 | 5 | 29-Jul-14 | 04-Aug-14 | 35 |
| L12-8118 | Elec Specialties Trim / Finish | 4 | 4 | 29-Jul-14 | 01-Aug-14 | 38 |
| L14-8107 | Final Coat Finish Paint | 5 | 5 | 29-Jul-14 | 04-Aug-14 | 30 |
| L16-8128 | Install Tub Glazing | 4 | 4 | 29-Jul-14 | 01-Aug-14 | 20 |
| L11-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 30-Jul-14 | 0 |
| L11-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 3 |
| L11-8134 | Pre-Clean Guestrooms | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 0 |
| L15-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 31-Jul-14 | 04-Aug-14 | 25 |
| L16-8105 | First Coat Finish Paint | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 20 |
| L17-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 15 |
| L14-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 01-Aug-14 | 07-Aug-14 | 34 |
| L14-8108 | Elec Trim / Finish | 5 | 5 | 01-Aug-14 | 07-Aug-14 | 34 |
| L14-8110 | HVAC Trim / Finish | 5 | 5 | 01-Aug-14 | 07-Aug-14 | 34 |
| L14-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 01-Aug-14 | 07-Aug-14 | 34 |
| L12-8114 | Signage (By Owner) | 3 | 3 | 04-Aug-14 | 06-Aug-14 | 35 |
| L16-8124 | Flooring @ Guest Rooms | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 20 |
| L17-8116 | Install Wood Base | 3 | 3 | 04-Aug-14 | 06-Aug-14 | 15 |
| L14-8126 | Doors & Hardware | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 30 |
| L14-8118 | Elec Specialties Trim / Finish | 4 | 4 | 05-Aug-14 | 08-Aug-14 | 33 |
| L15-8107 | Final Coat Finish Paint | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 25 |
| L17-8128 | Install Tub Glazing | 4 | 4 | 05-Aug-14 | 08-Aug-14 | 15 |
| L12-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 06-Aug-14 | 35 |
| L12-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 38 |

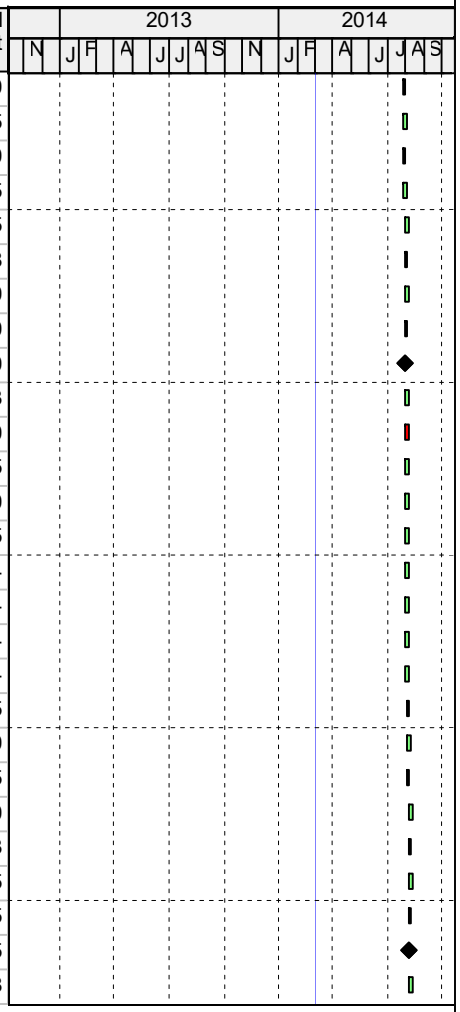



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8134 | Pre-Clean Guestrooms | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 35 |
| L16-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 07-Aug-14 | 11-Aug-14 | 20 |
| L17-8105 | First Coat Finish Paint | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 15 |
| L15-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 29 |
| L15-8108 | Elec Trim / Finish | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 29 |
| L15-8110 | HVAC Trim / Finish | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 29 |
| L15-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 29 |
| L14-8114 | Signage (By Owner) | 3 | 3 | 11-Aug-14 | 13-Aug-14 | 30 |
| L17-8124 | Flooring @ Guest Rooms | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 15 |
| L15-8126 | Doors & Hardware | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 25 |
| L15-8118 | Elec Specialties Trim / Finish | 4 | 4 | 12-Aug-14 | 15-Aug-14 | 28 |
| L16-8107 | Final Coat Finish Paint | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 20 |
| L14-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 13-Aug-14 | 30 |
| L14-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 33 |
| L14-8134 | Pre-Clean Guestrooms | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 30 |
| L17-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 14-Aug-14 | 18-Aug-14 | 15 |
| L16-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 24 |
| L16-8108 | Elec Trim / Finish | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 24 |
| L16-8110 | HVAC Trim / Finish | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 24 |
| L16-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 24 |
| L15-8114 | Signage (By Owner) | 3 | 3 | 18-Aug-14 | 20-Aug-14 | 25 |
| L16-8126 | Doors & Hardware | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 20 |
| L16-8118 | Elec Specialties Trim / Finish | 4 | 4 | 19-Aug-14 | 22-Aug-14 | 23 |
| L17-8107 | Final Coat Finish Paint | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 15 |
| L15-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 20-Aug-14 | 25 |
| L15-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 28 |
| L15-8134 | Pre-Clean Guestrooms | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 25 |

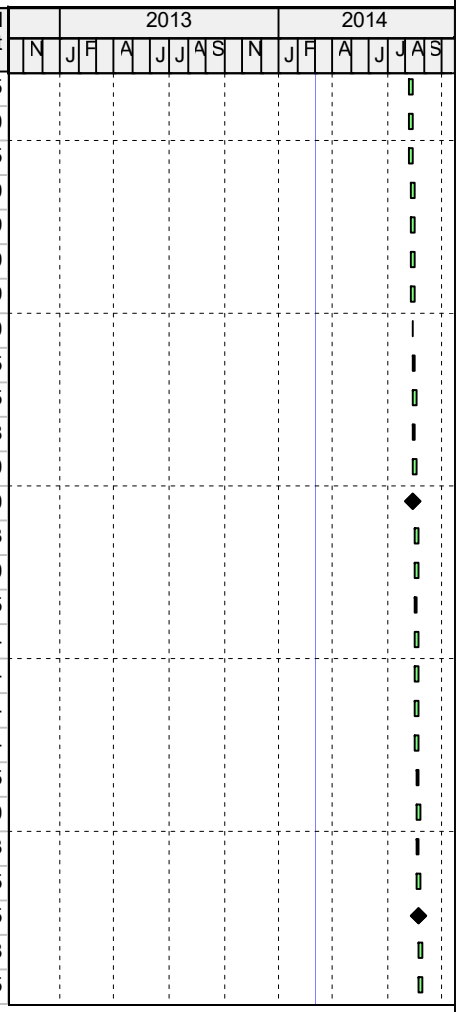



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 19 |
| L17-8108 | Elec Trim / Finish | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 19 |
| L17-8110 | HVAC Trim / Finish | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 19 |
| L17-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 19 |
| L16-8114 | Signage (By Owner) | 3 | 3 | 25-Aug-14 | 27-Aug-14 | 20 |
| L17-8126 | Doors & Hardware | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 15 |
| L17-8118 | Elec Specialties Trim / Finish | 4 | 4 | 26-Aug-14 | 29-Aug-14 | 18 |
| L16-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 27-Aug-14 | 20 |
| L16-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 23 |
| L16-8134 | Pre-Clean Guestrooms | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 20 |
| L17-8114 | Signage (By Owner) | 3 | 3 | 02-Sep-14 | 04-Sep-14 | 15 |
| L17-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 04-Sep-14 | 15 |
| L17-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 05-Sep-14 | 11-Sep-14 | 18 |
| L17-8134 | Pre-Clean Guestrooms | 5 | 5 | 05-Sep-14 | 11-Sep-14 | 15 |
| **Pool Area** | | | | | | |
| L03-8216 | L3 - Pool Surfaces / Finishes | 16 | 16 | 12-Aug-14 | 03-Sep-14 | 21 |
| L03-8218 | L3 - Pool Equipment | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 21 |
| **Corridors / Common / Public Areas** | | | | | | |
| L03-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 16-May-14 | 22-May-14 | 84 |
| L03-8206 | Flooring @ Corridors | 2 | 2 | 16-May-14 | 19-May-14 | 80 |
| L03-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 23-May-14 | 27-May-14 | 85 |
| L03-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 23-May-14 | 27-May-14 | 85 |
| L04-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 23-May-14 | 30-May-14 | 79 |
| L04-8206 | Flooring @ Corridors | 2 | 2 | 23-May-14 | 27-May-14 | 75 |
| L04-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 02-Jun-14 | 03-Jun-14 | 80 |
| L04-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 02-Jun-14 | 03-Jun-14 | 80 |
| L05-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 02-Jun-14 | 06-Jun-14 | 74 |

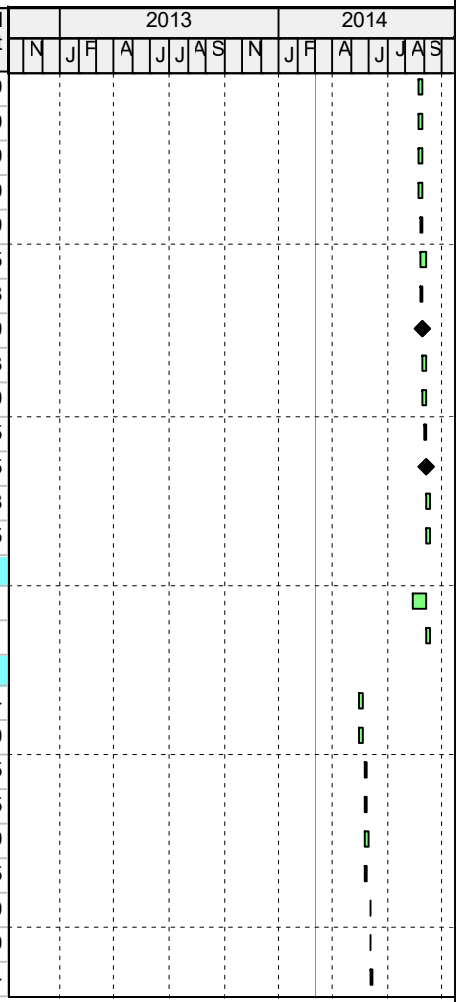



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8206 | Flooring @ Corridors | 2 | 2 | 02-Jun-14 | 03-Jun-14 | 70 |
| L05-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 09-Jun-14 | 10-Jun-14 | 75 |
| L05-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 09-Jun-14 | 10-Jun-14 | 75 |
| L06-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 09-Jun-14 | 13-Jun-14 | 69 |
| L06-8206 | Flooring @ Corridors | 2 | 2 | 09-Jun-14 | 10-Jun-14 | 65 |
| L03-8208 | Final Clean | 3 | 3 | 11-Jun-14 | 13-Jun-14 | 80 |
| L03-8210 | Owner Walk / Create Punchlist | 1 | 1 | 16-Jun-14 | 16-Jun-14 | 80 |
| L06-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 16-Jun-14 | 17-Jun-14 | 70 |
| L06-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 16-Jun-14 | 17-Jun-14 | 70 |
| L07-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 16-Jun-14 | 20-Jun-14 | 64 |
| L07-8206 | Flooring @ Corridors | 2 | 2 | 16-Jun-14 | 17-Jun-14 | 60 |
| L03-8212 | Resolve Final Punchlist | 5 | 5 | 17-Jun-14 | 23-Jun-14 | 80 |
| L04-8208 | Final Clean | 3 | 3 | 18-Jun-14 | 20-Jun-14 | 75 |
| L04-8210 | Owner Walk / Create Punchlist | 1 | 1 | 23-Jun-14 | 23-Jun-14 | 75 |
| L07-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 23-Jun-14 | 24-Jun-14 | 65 |
| L07-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 23-Jun-14 | 24-Jun-14 | 65 |
| L08-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 23-Jun-14 | 27-Jun-14 | 59 |
| L08-8206 | Flooring @ Corridors | 2 | 2 | 23-Jun-14 | 24-Jun-14 | 55 |
| L03-8214 | Floor Complete | 0 | 0 | | 23-Jun-14 | 80 |
| L04-8212 | Resolve Final Punchlist | 5 | 5 | 24-Jun-14 | 30-Jun-14 | 75 |
| L05-8208 | Final Clean | 3 | 3 | 25-Jun-14 | 27-Jun-14 | 70 |
| L05-8210 | Owner Walk / Create Punchlist | 1 | 1 | 30-Jun-14 | 30-Jun-14 | 70 |
| L08-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 30-Jun-14 | 01-Jul-14 | 60 |
| L08-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 30-Jun-14 | 01-Jul-14 | 60 |
| L09-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 30-Jun-14 | 07-Jul-14 | 54 |
| L09-8206 | Flooring @ Corridors | 2 | 2 | 30-Jun-14 | 01-Jul-14 | 50 |
| L04-8214 | Floor Complete | 0 | 0 | | 30-Jun-14 | 75 |

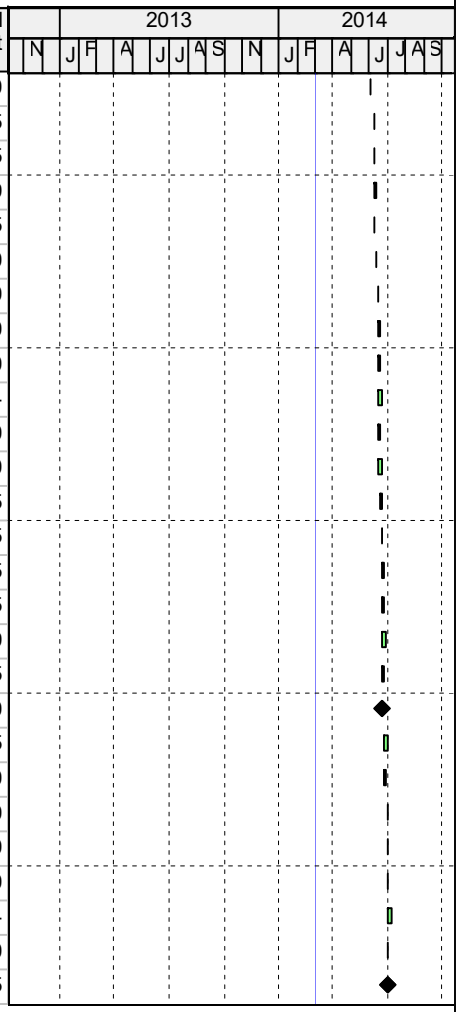



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8212 | Resolve Final Punchlist | 5 | 5 | 01-Jul-14 | 08-Jul-14 | 70 |
| L06-8208 | Final Clean | 3 | 3 | 02-Jul-14 | 07-Jul-14 | 65 |
| L06-8210 | Owner Walk / Create Punchlist | 1 | 1 | 08-Jul-14 | 08-Jul-14 | 65 |
| L09-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 08-Jul-14 | 09-Jul-14 | 55 |
| L09-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 08-Jul-14 | 09-Jul-14 | 55 |
| L10-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 08-Jul-14 | 14-Jul-14 | 49 |
| L10-8206 | Flooring @ Corridors | 2 | 2 | 08-Jul-14 | 09-Jul-14 | 45 |
| L05-8214 | Floor Complete | 0 | 0 | | 08-Jul-14 | 70 |
| L06-8212 | Resolve Final Punchlist | 5 | 5 | 09-Jul-14 | 15-Jul-14 | 65 |
| L07-8208 | Final Clean | 3 | 3 | 10-Jul-14 | 14-Jul-14 | 60 |
| L07-8210 | Owner Walk / Create Punchlist | 1 | 1 | 15-Jul-14 | 15-Jul-14 | 60 |
| L10-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 50 |
| L10-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 50 |
| L11-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 4 |
| L11-8206 | Flooring @ Corridors | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 0 |
| L06-8214 | Floor Complete | 0 | 0 | | 15-Jul-14 | 65 |
| L07-8212 | Resolve Final Punchlist | 5 | 5 | 16-Jul-14 | 22-Jul-14 | 60 |
| L08-8208 | Final Clean | 3 | 3 | 17-Jul-14 | 21-Jul-14 | 55 |
| L08-8210 | Owner Walk / Create Punchlist | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 55 |
| L11-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 22-Jul-14 | 23-Jul-14 | 5 |
| L11-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 22-Jul-14 | 23-Jul-14 | 5 |
| L12-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 22-Jul-14 | 28-Jul-14 | 39 |
| L12-8206 | Flooring @ Corridors | 2 | 2 | 22-Jul-14 | 23-Jul-14 | 35 |
| L07-8214 | Floor Complete | 0 | 0 | | 22-Jul-14 | 60 |
| L08-8212 | Resolve Final Punchlist | 5 | 5 | 23-Jul-14 | 29-Jul-14 | 55 |
| L09-8208 | Final Clean | 3 | 3 | 24-Jul-14 | 28-Jul-14 | 50 |
| L09-8210 | Owner Walk / Create Punchlist | 1 | 1 | 29-Jul-14 | 29-Jul-14 | 50 |

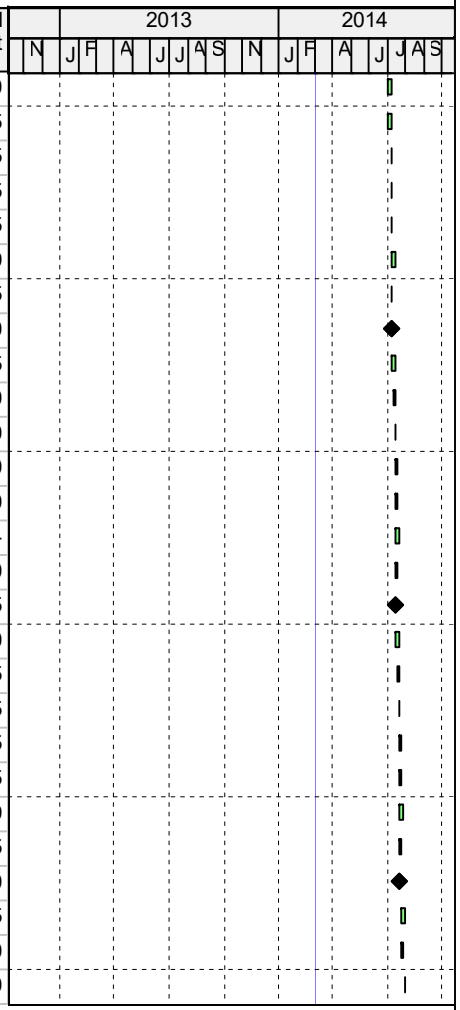



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 29-Jul-14 | 30-Jul-14 | 40 |
| L12-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 29-Jul-14 | 30-Jul-14 | 40 |
| L14-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 29-Jul-14 | 04-Aug-14 | 34 |
| L14-8206 | Flooring @ Corridors | 2 | 2 | 29-Jul-14 | 30-Jul-14 | 30 |
| L08-8214 | Floor Complete | 0 | 0 | | 29-Jul-14 | 55 |
| L09-8212 | Resolve Final Punchlist | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 50 |
| L10-8208 | Final Clean | 3 | 3 | 31-Jul-14 | 04-Aug-14 | 45 |
| L10-8210 | Owner Walk / Create Punchlist | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 45 |
| L14-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 05-Aug-14 | 06-Aug-14 | 35 |
| L14-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 05-Aug-14 | 06-Aug-14 | 35 |
| L15-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 29 |
| L15-8206 | Flooring @ Corridors | 2 | 2 | 05-Aug-14 | 06-Aug-14 | 25 |
| L09-8214 | Floor Complete | 0 | 0 | | 05-Aug-14 | 50 |
| L10-8212 | Resolve Final Punchlist | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 45 |
| L11-8208 | Final Clean | 3 | 3 | 07-Aug-14 | 11-Aug-14 | 0 |
| L11-8210 | Owner Walk / Create Punchlist | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 0 |
| L15-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 30 |
| L15-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 30 |
| L16-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 24 |
| L16-8206 | Flooring @ Corridors | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 20 |
| L10-8214 | Floor Complete | 0 | 0 | | 12-Aug-14 | 45 |
| L11-8212 | Resolve Final Punchlist | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 0 |
| L12-8208 | Final Clean | 3 | 3 | 14-Aug-14 | 18-Aug-14 | 35 |
| L12-8210 | Owner Walk / Create Punchlist | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 35 |
| L16-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 19-Aug-14 | 20-Aug-14 | 25 |
| L16-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 19-Aug-14 | 20-Aug-14 | 25 |
| L17-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 19 |

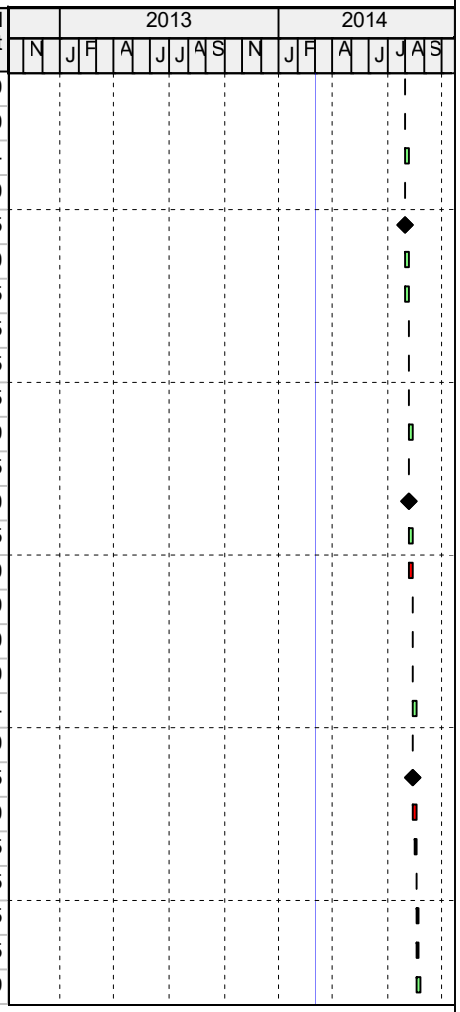



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8206 | Flooring @ Corridors | 2 | 2 | 19-Aug-14 | 20-Aug-14 | 15 |
| L11-8214 | Floor Complete | 0 | 0 | | 19-Aug-14 | 0 |
| L12-8212 | Resolve Final Punchlist | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 35 |
| L14-8208 | Final Clean | 3 | 3 | 21-Aug-14 | 25-Aug-14 | 30 |
| L14-8210 | Owner Walk / Create Punchlist | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 30 |
| L17-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 26-Aug-14 | 27-Aug-14 | 20 |
| L17-8204 | Mech Trim / Finish @ Corridors | 2 | 2 | 26-Aug-14 | 27-Aug-14 | 20 |
| L12-8214 | Floor Complete | 0 | 0 | | 26-Aug-14 | 35 |
| L14-8212 | Resolve Final Punchlist | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 30 |
| L15-8208 | Final Clean | 3 | 3 | 28-Aug-14 | 02-Sep-14 | 25 |
| L15-8210 | Owner Walk / Create Punchlist | 1 | 1 | 03-Sep-14 | 03-Sep-14 | 25 |
| L14-8214 | Floor Complete | 0 | 0 | | 03-Sep-14 | 30 |
| L15-8212 | Resolve Final Punchlist | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 25 |
| L16-8208 | Final Clean | 3 | 3 | 05-Sep-14 | 09-Sep-14 | 20 |
| L16-8210 | Owner Walk / Create Punchlist | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 20 |
| L15-8214 | Floor Complete | 0 | 0 | | 10-Sep-14 | 25 |
| L16-8212 | Resolve Final Punchlist | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 20 |
| L17-8208 | Final Clean | 3 | 3 | 12-Sep-14 | 16-Sep-14 | 15 |
| L17-8210 | Owner Walk / Create Punchlist | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 15 |
| L16-8214 | Floor Complete | 0 | 0 | | 17-Sep-14 | 20 |
| L17-8212 | Resolve Final Punchlist | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 15 |
| L17-8214 | Floor Complete | 0 | 0 | | 24-Sep-14 | 15 |
| **Mech Penthouse** | | | | | | |
| PH-8100 | PH - Insulation | 3 | 3 | 26-Jun-14 | 30-Jun-14 | 37 |
| PH-8102 | PH - GWB Hang / Tape / Finish - (Including Common | 10 | 10 | 01-Jul-14 | 15-Jul-14 | 37 |
| PH-8104 | PH - Int Painting | 4 | 4 | 11-Jul-14 | 16-Jul-14 | 37 |
| PH-8108 | PH - Elec Trim / Finish | 10 | 10 | 17-Jul-14 | 30-Jul-14 | 37 |

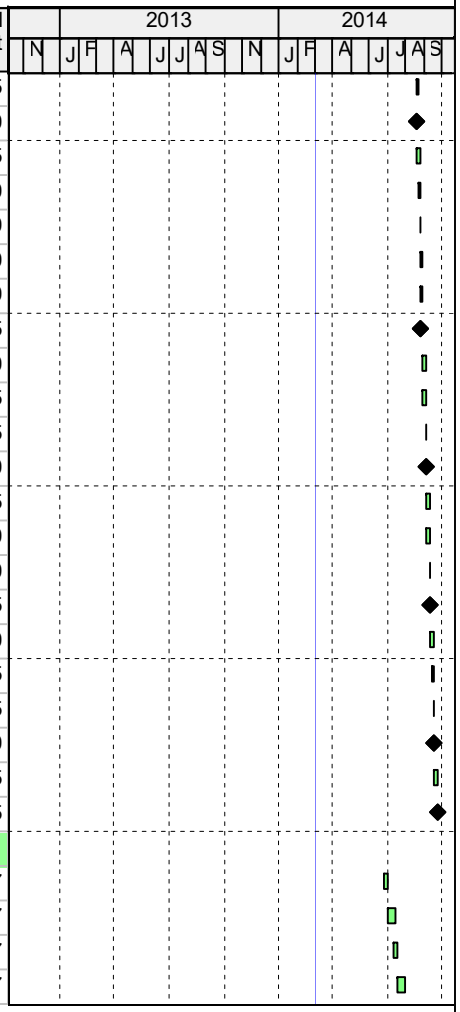



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-8110 | PH - HVAC Trim / Finish | 10 | 10 | 17-Jul-14 | 30-Jul-14 | 37 |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 5 | 5 | 17-Jul-14 | 23-Jul-14 | 42 |
| PH-8114 | PH - Signage | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 53 |
| PH-8118 | PH - Elec Specialties Trim / Finish | 4 | 4 | 17-Jul-14 | 22-Jul-14 | 43 |
| PH-8116 | PH - Finish Carpentry / Millwork | 5 | 5 | 18-Jul-14 | 24-Jul-14 | 41 |
| PH-8122 | PH - Plumbing Trim / Finish | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 42 |
| PH-8124 | PH - Flooring | 4 | 4 | 31-Jul-14 | 05-Aug-14 | 37 |
| PH-8126 | PH - Doors & Hardware | 3 | 3 | 04-Aug-14 | 06-Aug-14 | 37 |
| PH-8130 | PH - Guest Rooms Substantially Complete | 0 | 0 | | 06-Aug-14 | 37 |
| PH-8132 | PH - Contractor Pre-Punchlist | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 38 |
| PH-8134 | PH - Pre-Clean | 3 | 3 | 07-Aug-14 | 11-Aug-14 | 37 |
| PH-8208 | PH - Final Clean | 3 | 3 | 12-Aug-14 | 14-Aug-14 | 37 |
| PH-8210 | PH - Owner Walk / Create Punchlist | 1 | 1 | 15-Aug-14 | 15-Aug-14 | 37 |
| PH-8212 | PH - Final Punchlist | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 37 |
| PH-8214 | PH - Floor Complete | 0 | 0 | | 22-Aug-14 | 37 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| **Smoke Control** | | | | | | |
| CO-7104 | Smoke Control Pre-Testing | 10 | 10 | 08-Sep-14 | 19-Sep-14 | 8 |
| CO-7106 | City of Bellevue Smoke Control Testing | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 8 |
| CO-7108 | Final Marriott Smoke Control Testing | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 8 |
| **Fire Sprinklers** | | | | | | |
| CO-7110 | Fire Sprinkler Pre-Testing | 10 | 10 | 08-Sep-14 | 19-Sep-14 | 8 |
| CO-7112 | City of Bellevue Fire Sprinkler Inspection / Approval | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 8 |
| CO-7114 | Marriott Fire Sprinkler Testing | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 8 |
| **Fire Alarm** | | | | | | |
| CO-7116 | Fire Alarm Pre-Testing | 10 | 10 | 08-Sep-14 | 18-Sep-14 | 12 |
| CO-7118 | City of Bellevue Fire Alarm Inspection / Approval | 5 | 5 | 19-Sep-14 | 25-Sep-14 | 10 |

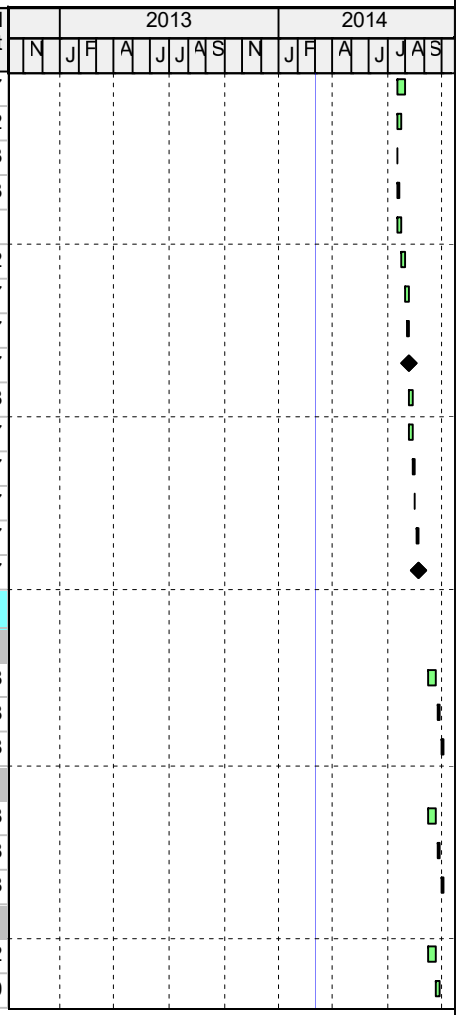



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7120 | Marriott Fire Alarm Testing | 5 | 5 | 26-Sep-14 | 01-Oct-14 | 12 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| CO-7100 | CO - Preliminary Start-Up & Testing | 15 | 15 | 15-Aug-14 | 05-Sep-14 | 8 |
| CO-7102 | CO - HVAC Commissioning | 10 | 10 | 08-Sep-14 | 19-Sep-14 | 18 |





© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Working Schedule - 6-5-14 Update** | | | | | | |
| I-1500 | Owner release revised LV design - Tower (ASIs 5, 13, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-1550 | Owner release revised LV design - Podium (ASIs 5, 1 | 200 | 0 | 23-May-13 A | 28-Apr-14 A | |
| I-1900 | Owner issue design revisions (ASIs 4, 9, 19, 34) | 215 | 0 | 23-May-13 A | 24-Mar-14 A | |
| I-2500 | Owner issue LL1 electrical revisions (ASIs 7, 9r2, 14, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-3400 | Owner provide Level 2 ceiling heights | 180 | 0 | 24-Jun-13 A | 24-Mar-14 A | |
| I-3700 | Owner resolve wall condition between stair and Eleva | 200 | 6 | 27-Jun-13 A | 12-Jun-14 | 2 |
| MM-1000 | MM - Temporary Power Available | 0 | 0 | 08-Jul-13 A | | |
| I-2100 | Owner revise roof steel design (Submittals 365, 370, | 200 | 0 | 09-Jul-13 A | 07-Apr-14 A | |
| I-2200 | Owner resolve elevator steel issue (RFI 112, RFI 112. | 200 | 0 | 09-Jul-13 A | 03-Mar-14 A | |
| I-2400 | Owner provide Tower light fixture selections (ASI 36) | 185 | 0 | 18-Jul-13 A | 08-Apr-14 A | |
| I-2900 | Owner revise Food Service and Kitchen (ASIs 11, 12, | 140 | 0 | 08-Aug-13 A | 27-Feb-14 A | |
| I-1400 | Owner develop envelope redesign | 70 | 0 | 27-Aug-13 A | 12-Dec-13 A | |
| I-3600 | Owner closeout glass/glazing allowance | 160 | 0 | 04-Sep-13 A | 30-Apr-14 A | |
| I-1200 | Owner release revised Concierge Lounge design (AS | 160 | 0 | 06-Sep-13 A | 08-Apr-14 A | |
| I-2800 | Owner revise interior public space design (ASIs 16, 1 | 130 | 0 | 25-Sep-13 A | 09-Apr-14 A | |
| I-2000 | Owner approve door frames (Submittals 258, 454, 48 | 85 | 0 | 27-Sep-13 A | 23-Jan-14 A | |
| I-3100 | Owner revise ballroom ceiling design (ASIs 18, 25) | 100 | 0 | 17-Oct-13 A | 25-Feb-14 A | |
| I-1600 | Owner provide directive for south & east corridor encl | 110 | 0 | 28-Oct-13 A | 18-Apr-14 A | |
| I-2300 | Owner resolve fire smoke dampers issue (RFI 233) | 115 | 0 | 30-Oct-13 A | 11-Apr-14 A | |
| I-2600 | Owner resolve L2 slab coordination issue | 4 | 0 | 13-Nov-13 A | 16-Nov-13 A | |
| I-2700 | Owner revise tower guest rooms design (ASIs 23, 29) | 58 | 0 | 04-Dec-13 A | 26-Feb-14 A | |
| I-1700 | Owner provide design for dry site utilities (ASIs 20, 20 | 66 | 0 | 09-Dec-13 A | 13-Mar-14 A | |
| I-1402 | Begin exterior panel production | 41 | 0 | 13-Dec-13 A | 12-Feb-14 A | |
| I-1300 | Owner issue "Hold" directive (email) | 0 | 0 | | 19-Dec-13 A | |
| I-1100 | Owner release revised L17 design (ASI 23, 29R1) | 74 | 0 | 20-Dec-13 A | 08-Apr-14 A | |
| I-1302 | Owner issue ASI 30 (Prep Kitchen Revisions) | 47 | 0 | 20-Dec-13 A | 27-Feb-14 A | |

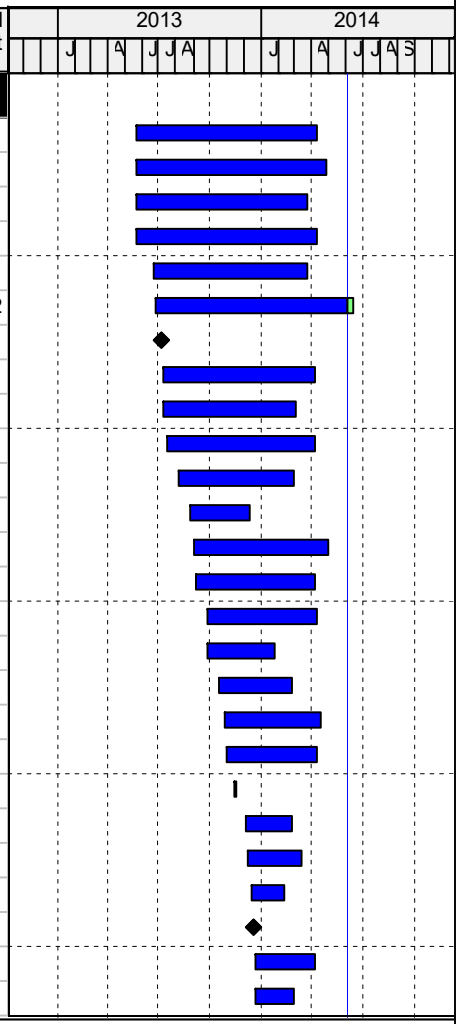


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| High Rise Hotel Sample Project | All Activities | Schedule Status Date 05-Jun-14 |
|---|---|---|

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1404 | City of Bellevue Approval | 90 | 7 | 23-Dec-13 A | 13-Jun-14 | 65 |
| I-3000 | Owner revise bar area (change to straight bar, IDRFI-( | 71 | 0 | 22-Jan-14 A | 27-May-14 A | |
| I-2202 | Fabricate revised elevator steel | 60 | 0 | 04-Mar-14 A | 07-May-14 A | |
| I-2704 | Framing "Go Back" work for ASIs 23, 29 - L4 | 1 | 0 | 05-Mar-14 A | 12-Mar-14 A | |
| I-3900 | RFI 471, Resolve Ballroom parapet height issue | 1 | 0 | 08-Mar-14 A | 07-May-14 A | |
| I-1702 | Owner provide directive to proceed | 26 | 0 | 14-Mar-14 A | 01-May-14 A | |
| I-3300 | Owner provide Guest Room plumbing fixture selectio | 1 | 0 | 20-Mar-14 A | 20-Mar-14 A | |
| I-1902 | Procure revised structural steel | 15 | 0 | 25-Mar-14 A | 14-Apr-14 A | |
| I-4000 | Owner complete design of east stitched enclosure (fo | 1 | 0 | 01-Apr-14 A | 14-May-14 A | |
| I-2102 | Fabricate revised roof steel | 20 | 0 | 08-Apr-14 A | 15-May-14 A | |
| I-3200 | Owner provide light fixture selections for podium level | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| I-3800 | Resolve Heat Pump Electrical Overcurrent Issue | 20 | 2 | 23-Apr-14 A | 06-Jun-14 | 49 |
| L10-8221 | HVAC Risers Duct Insulation | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L11-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| I-2304 | Framing "Go Back" work at L3 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2308 | Framing "Go Back" work at L5 for RFI 233 | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2706 | Framing "Go Back" work for ASIs 23, 29 - L5 | 1 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2708 | Framing "Go Back" work for ASIs 23, 29 - L6 | 1 | 0 | 29-Apr-14 A | 09-May-14 A | |
| I-2702 | Framing "Go Back" work for ASIs 23, 29 - L3 | 1 | 0 | 01-May-14 A | 01-May-14 A | |
| I-1706 | PSE scheduling delay | 10 | 0 | 01-May-14 A | 20-May-14 A | |
| I-3602 | Complete shop drawings & fab/deliver storefront fram | 40 | 27 | 01-May-14 A | 14-Jul-14 | 8 |
| L04-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| I-1802 | Rework framing for door hold-opens - LL4 | 1 | 0 | 07-May-14 A | 08-May-14 A | |
| L04-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-May-14 A | 12-May-14 A | |
| I-1800 | Owner issue directive to proceed with door hold-open | 1 | 0 | 08-May-14 A | 08-May-14 A | |
| I-1804 | Rework framing for door hold-opens - LL3 | 1 | 0 | 08-May-14 A | 09-May-14 A | |

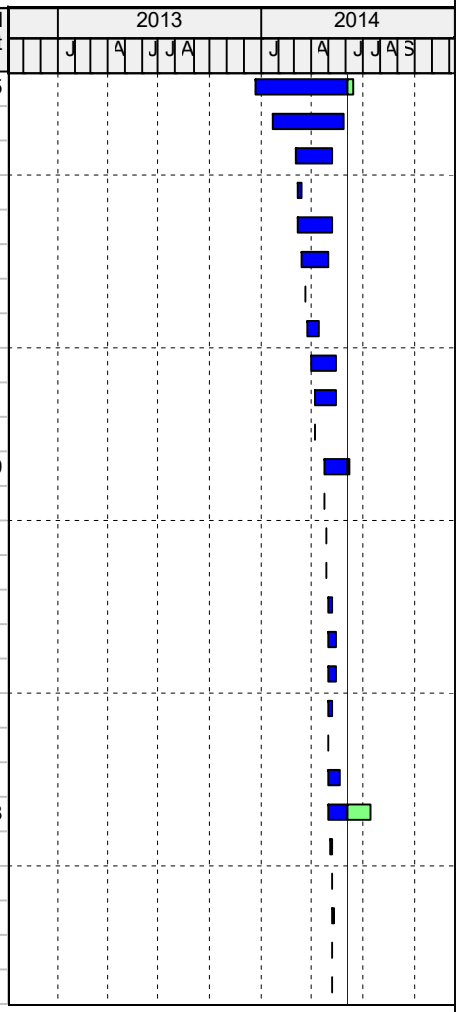


Actual Work  Critical Remai...
Remaining Work  Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-2312 | Framing "Go Back" work at L7 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-3902 | Install Ballroom parapet extension | 5 | 0 | 08-May-14 A | 13-May-14 A | |
| I-1806 | Rework framing for door hold-opens - LL2 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-1808 | Rework framing for door hold-opens - LL1 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-2310 | Framing "Go Back" work at L6 for RFI 233 | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| I-2710 | Framing "Go Back" work for ASIs 23, 29 - L7 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| L05-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L06-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L05-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| MP-FAB1 | Fabricate and Deliver Bronze Gold Horizontal Panels | 30 | 13 | 12-May-14 A | 23-Jun-14 | 59 |
| MP-FAB2 | Fabricate and Deliver Silver Vertical Panels | 45 | 27 | 12-May-14 A | 14-Jul-14 | 60 |
| PH-8704 | PH - Install Machine Support Steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| PH-8710 | Install elevator rail support steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| L03-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L03-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 13-May-14 A | 14-May-14 A | |
| I-4002 | East Stitched - Install framing and windows | 9 | 7 | 19-May-14 A | 13-Jun-14 | 110 |
| L10-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L11-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L12-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| RF-4038 | AR - Concrete pads and curbs | 5 | 0 | 21-May-14 A | 04-Jun-14 A | |
| L10-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L11-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L12-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L14-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L15-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 27-May-14 A | |

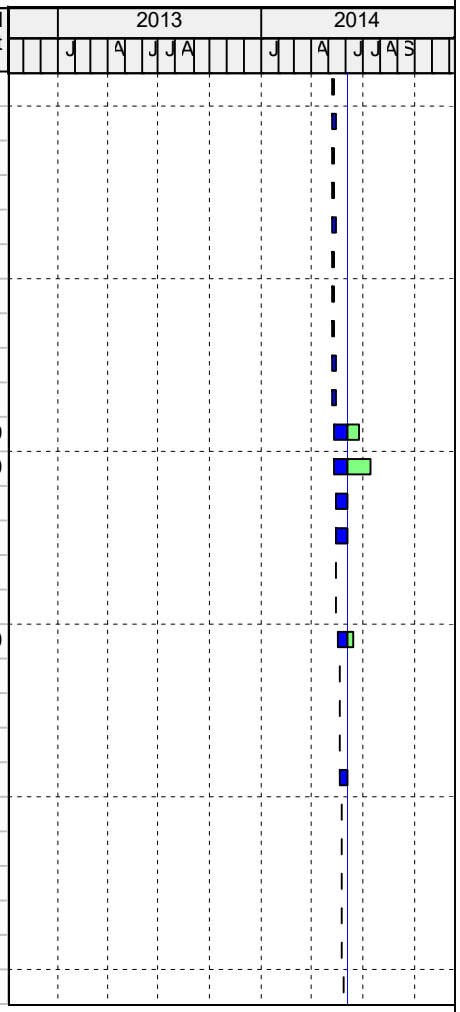



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 3 | 27-May-14 A | 09-Jun-14 | 46 |
| L12-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 1 | 27-May-14 A | 05-Jun-14 | 124 |
| L07-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 1 | 27-May-14 A | 05-Jun-14 | 55 |
| L07-6036 | Framing Around Heat Pump & Soffit | 3 | 2 | 27-May-14 A | 06-Jun-14 | 53 |
| I-3002 | City of Bellevue approve bar design changes. | 5 | 1 | 28-May-14 A | 05-Jun-14 | 20 |
| L16-8221 | HVAC Risers Duct Insulation | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| PH-8712 | PH - Complete Framing and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| PH-8714 | Stage PH/L18 roofing materials | 2 | 0 | 30-May-14 A | 30-May-14 A | |
| L08-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L08-6036 | Framing Around Heat Pump & Soffit | 3 | 1 | 02-Jun-14 A | 05-Jun-14 | 54 |
| PH-8704I | Correct support steel embeds | 2 | 0 | 02-Jun-14 A | 04-Jun-14 A | |
| L14-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 03-Jun-14 A | 04-Jun-14 A | |
| L17-8221 | HVAC Risers Duct Insulation | 1 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| RF-6028 | Tower Roof - Structural Steel | 5 | 5 | 04-Jun-14 A | 11-Jun-14 | 11 |
| L14-6027 | Electrical to Fire/Smoke Dampers | 1 | 1 | 05-Jun-14 | 05-Jun-14 | 16 |
| L15-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 2 | 05-Jun-14 | 06-Jun-14 | 118 |
| L06-6040 | Test Heat Pumps - L3, L4, L5 and L6 | 3 | 3 | 05-Jun-14 | 09-Jun-14 | 42 |
| LL2-2046 | LL2 - Generator Room build-out | 20 | 20 | 05-Jun-14 | 02-Jul-14 | 87 |
| LL1-6014Ia | L1 bar redesign - rework plumbing at ceilings | 1 | 1 | 05-Jun-14 | 05-Jun-14 | 20 |
| LL2-2052 | LL2 - Install fuel piping and exhaust duct to Generatc | 5 | 5 | 05-Jun-14* | 11-Jun-14 | 62 |
| PC-4010 | PC - Fireproof Entry Roof Steel | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 17 |
| LL1-6005 | Head of Wall Fire Caulk at CMU | 2 | 2 | 05-Jun-14 | 06-Jun-14 | 9 |
| L1B-6005 | Head of Wall Fire Caulk at CMU (including East Servic | 2 | 2 | 05-Jun-14 | 06-Jun-14 | 5 |
| L1K-6005 | Head of Wall Fire Caulk at CMU (including public restr | 2 | 2 | 05-Jun-14 | 06-Jun-14 | 7 |
| L04-6005 | CMU Fire Caulk/Clips | 2 | 2 | 05-Jun-14 | 06-Jun-14 | 37 |
| L05-6005 | CMU Fire Caulk/Clips | 2 | 2 | 05-Jun-14 | 06-Jun-14 | 47 |
| L06-6005 | CMU Fire Caulk/Clips | 2 | 2 | 05-Jun-14 | 06-Jun-14 | 49 |

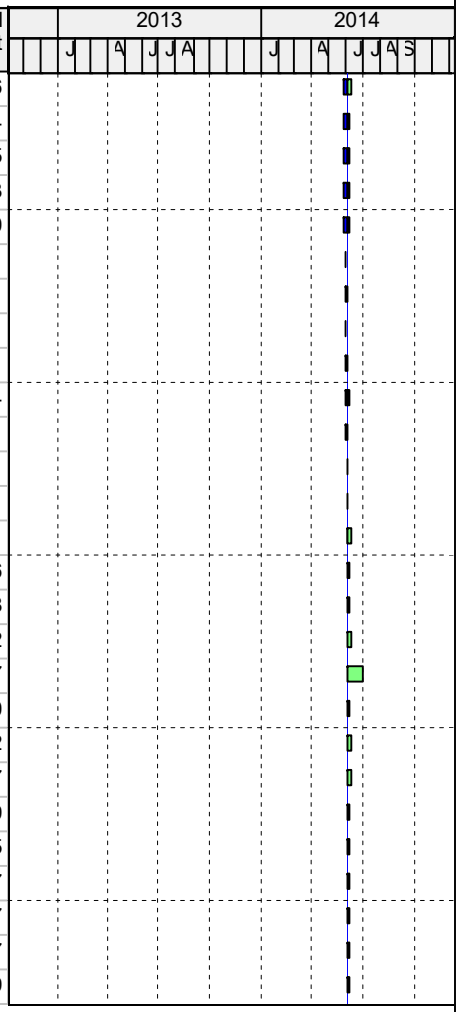



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6005 | CMU Fire Caulk/Clips | 2 | 2 | 05-Jun-14 | 06-Jun-14 | 54 |
| L08-6005 | CMU Fire Caulk/Clips | 2 | 2 | 05-Jun-14 | 06-Jun-14 | 54 |
| L09-6005 | CMU Fire Caulk/Clips | 2 | 2 | 05-Jun-14 | 06-Jun-14 | 61 |
| L10-6005 | CMU Fire Caulk/Clips | 2 | 2 | 05-Jun-14 | 06-Jun-14 | 54 |
| L11-6005 | CMU Fire Caulk/Clips | 2 | 2 | 05-Jun-14 | 06-Jun-14 | 47 |
| L12-6005 | CMU Fire Caulk/Clips | 2 | 2 | 05-Jun-14 | 06-Jun-14 | 48 |
| L14-6005 | CMU Fire Caulk/Clips | 2 | 2 | 05-Jun-14 | 06-Jun-14 | 46 |
| L15-6005 | CMU Fire Caulk/Clips | 2 | 2 | 05-Jun-14 | 06-Jun-14 | 14 |
| L16-6005 | CMU Fire Caulk/Clips | 2 | 2 | 05-Jun-14 | 06-Jun-14 | 33 |
| L14-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 2 | 06-Jun-14 | 09-Jun-14 | 16 |
| L08-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 06-Jun-14 | 06-Jun-14 | 54 |
| LL1-6014Ib | L1 bar redesign - rework ceiling framing | 1 | 1 | 06-Jun-14 | 06-Jun-14 | 29 |
| L1B-6026 | Install operable partition track | 5 | 5 | 06-Jun-14 | 12-Jun-14 | 18 |
| I-1304 | Prep Kitchen - Additional framing (ASI 30) | 2 | 2 | 09-Jun-14 | 10-Jun-14 | 15 |
| I-2302 | Framing "Go Back" work at LL1 for RFI 233 | 3 | 3 | 09-Jun-14 | 11-Jun-14 | 35 |
| L15-6027 | Electrical to Fire/Smoke Dampers | 1 | 1 | 09-Jun-14 | 09-Jun-14 | 118 |
| L16-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 2 | 09-Jun-14 | 10-Jun-14 | 19 |
| L03-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 09-Jun-14 | 09-Jun-14 | 49 |
| L04-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 09-Jun-14 | 09-Jun-14 | 51 |
| L05-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 09-Jun-14 | 09-Jun-14 | 56 |
| L06-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 09-Jun-14 | 09-Jun-14 | 58 |
| L07-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 09-Jun-14 | 09-Jun-14 | 53 |
| LL1-Z2-6005 | Head of Wall Fire Caulk at CMU | 2 | 2 | 09-Jun-14 | 10-Jun-14 | 9 |
| L15-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 2 | 10-Jun-14 | 11-Jun-14 | 118 |
| L09-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 10-Jun-14 | 11-Jun-14 | 58 |
| L09-6036 | Framing Around Heat Pump & Soffit | 3 | 3 | 10-Jun-14 | 12-Jun-14 | 56 |
| L1L-6005 | Head of Wall Fire Caulk at CMU (including back of ho | 2 | 2 | 10-Jun-14 | 11-Jun-14 | 2 |

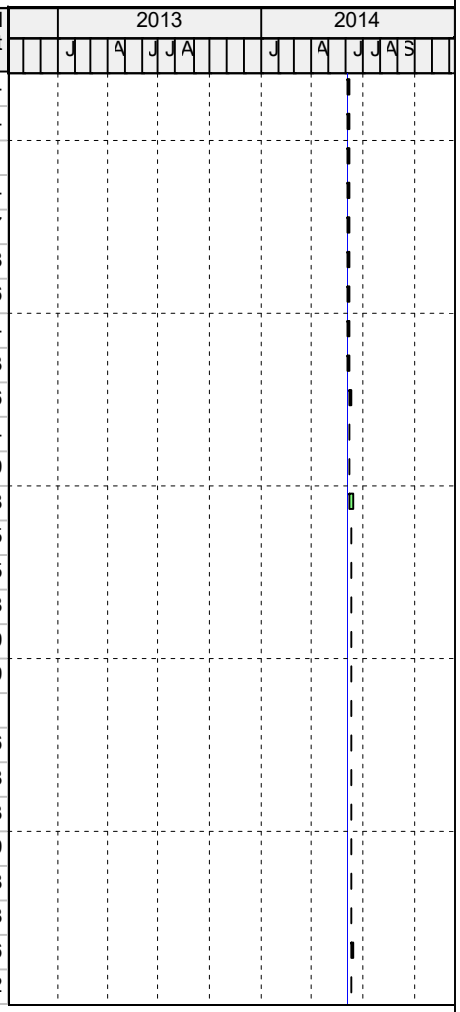



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6027 | Electrical to Fire/Smoke Dampers | 1 | 1 | 11-Jun-14 | 11-Jun-14 | 19 |
| LL1-Z3-6005 | Head of Wall Fire Caulk at CMU (At All Areas North of | 2 | 2 | 11-Jun-14 | 12-Jun-14 | 24 |
| I-2306 | Framing "Go Back" work at L4 for RFI 233 | 3 | 3 | 12-Jun-14 | 16-Jun-14 | 36 |
| L16-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 2 | 12-Jun-14 | 13-Jun-14 | 19 |
| L17-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 2 | 12-Jun-14 | 13-Jun-14 | 11 |
| RF-4008 | Tower Roof - Coping / Flashing | 10 | 10 | 12-Jun-14 | 25-Jun-14 | 102 |
| L09-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 13-Jun-14 | 13-Jun-14 | 56 |
| I-3702 | Complete wall framing at Stair/Elevator 5 (LL4) | 2 | 2 | 13-Jun-14 | 16-Jun-14 | 38 |
| I-3720 | Fireproof added steel between Stair 1 and Elevator 5 | 5 | 5 | 13-Jun-14 | 19-Jun-14 | 2 |
| L17-6027 | Electrical to Fire/Smoke Dampers | 1 | 1 | 16-Jun-14 | 16-Jun-14 | 11 |
| L10-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 16-Jun-14 | 17-Jun-14 | 54 |
| L10-6036 | Framing Around Heat Pump & Soffit | 3 | 3 | 16-Jun-14 | 18-Jun-14 | 52 |
| LL2-2048 | LL2 - Set Laundry Room equipment (BY OTHERS) | 2 | 2 | 16-Jun-14* | 17-Jun-14 | 108 |
| TC-5912 | Tower Crane pour-backs (LL4 to L3) | 4 | 4 | 16-Jun-14 | 19-Jun-14 | 32 |
| LL1-Z2-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 10 | 16-Jun-14 | 27-Jun-14 | 23 |
| I-4004 | East Stitched - Install metal panels | 5 | 5 | 16-Jun-14 | 20-Jun-14 | 110 |
| I-1306 | Prep Kitchen - Additional plumbing (ASI 30) | 4 | 4 | 17-Jun-14 | 20-Jun-14 | 25 |
| I-2314 | Framing "Go Back" work at L8 for RFI 233 | 3 | 3 | 17-Jun-14 | 19-Jun-14 | 45 |
| L17-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 2 | 17-Jun-14 | 18-Jun-14 | 11 |
| I-3704 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 5 | 17-Jun-14 | 23-Jun-14 | 38 |
| I-3706 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 5 | 17-Jun-14 | 23-Jun-14 | 38 |
| I-3708 | Complete wall framing at Stair/Elevator 5 (LL3) | 2 | 2 | 17-Jun-14 | 18-Jun-14 | 39 |
| L17-6005 | CMU Fire Caulk/Clips | 2 | 2 | 17-Jun-14 | 18-Jun-14 | 15 |
| LL2-2050 | LL2 - Laundry Room equipment final connections (MI | 10 | 10 | 18-Jun-14 | 01-Jul-14 | 108 |
| L10-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 19-Jun-14 | 19-Jun-14 | 52 |
| LL2E-8108 | LL2 - Set fire pumps and equipment | 5 | 5 | 19-Jun-14 | 25-Jun-14 | 41 |
| LL1-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 10 | 19-Jun-14 | 02-Jul-14 | 11 |

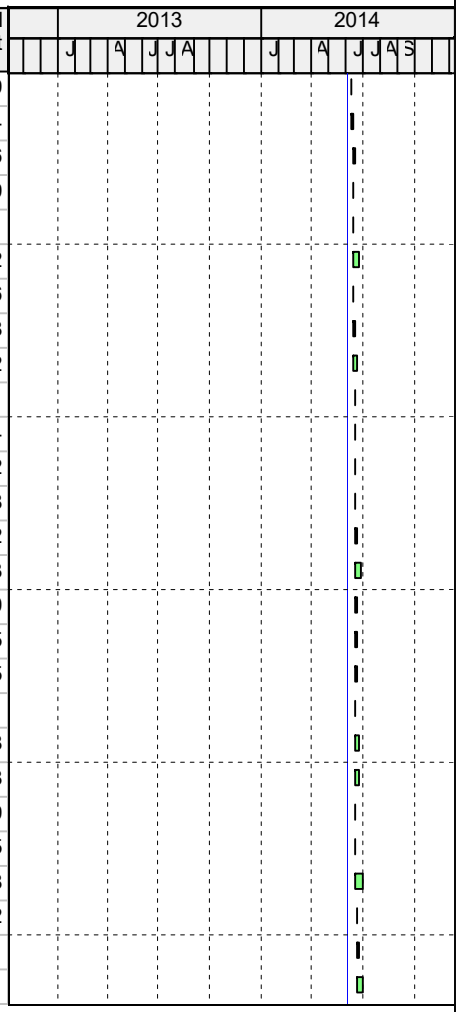



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-3710 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 5 | 19-Jun-14 | 25-Jun-14 | 39 |
| I-3712 | Complete remaining HVAC rough-in at Stair/Elevator : | 5 | 5 | 19-Jun-14 | 25-Jun-14 | 39 |
| L03-8600 | L3 Pool - Framing & HM frames | 5 | 5 | 19-Jun-14 | 25-Jun-14 | 66 |
| L11-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 20-Jun-14 | 23-Jun-14 | 43 |
| L11-6036 | Framing Around Heat Pump & Soffit | 3 | 3 | 20-Jun-14 | 24-Jun-14 | 41 |
| LL1-Z2-6018a | Complete Mech RI at tower crane opening (LL1) | 4 | 4 | 20-Jun-14 | 25-Jun-14 | 32 |
| I-3722 | Complete GWB between Stair 1 and Elevator 5 shaft | 10 | 10 | 20-Jun-14 | 03-Jul-14 | 2 |
| L10-6040 | Test Heat Pumps - L7, L8, L9 and L10 | 3 | 3 | 23-Jun-14 | 25-Jun-14 | 10 |
| I-2502 | Electrical rework at LL1 for ASIs 7, 9r2, 14, 27 | 1 | 1 | 24-Jun-14 | 24-Jun-14 | 26 |
| MPT-1000 | Tower - Initial West Elevation Metal Panels | 15 | 15 | 24-Jun-14 | 15-Jul-14 | 59 |
| MPP-1008 | Podium - East Elevation Metal Panels | 10 | 10 | 24-Jun-14 | 08-Jul-14 | 94 |
| MPT-1006 | Tower - East Elevation Grid FF-S Metal Panels | 15 | 15 | 24-Jun-14 | 15-Jul-14 | 59 |
| L11-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 25-Jun-14 | 25-Jun-14 | 41 |
| L12-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 26-Jun-14 | 27-Jun-14 | 46 |
| L12-6036 | Framing Around Heat Pump & Soffit | 3 | 3 | 26-Jun-14 | 30-Jun-14 | 45 |
| LL2E-8110 | LL2 - Electtrical, Fire pumps/equipment final connecti | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 41 |
| L03-8602 | L3 Pool - Fire Sprinkler R/I | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 66 |
| L03-8604 | L3 Pool - Plumbing R/I | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 66 |
| L03-8606 | L3 Pool - HVAC R/I | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 66 |
| L03-8608 | L3 Pool - Electrical R/I | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 66 |
| L03-8610 | L3 Pool - Fire Alarm / Elec Specialties R/I | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 66 |
| L12-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 30-Jun-14 | 30-Jun-14 | 45 |
| L14-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 01-Jul-14 | 02-Jul-14 | 43 |
| L14-6036 | Framing Around Heat Pump & Soffit | 3 | 3 | 01-Jul-14 | 03-Jul-14 | 41 |
| LL4-6005 | LL4 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 3 | 02-Jul-14 | 07-Jul-14 | 27 |
| LL3-6005 | LL3 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 3 | 02-Jul-14 | 07-Jul-14 | 30 |
| LL2-6005 | LL2 - Seismic Head Of Wall Fire Caulk at CMU | 5 | 5 | 02-Jul-14 | 09-Jul-14 | 28 |

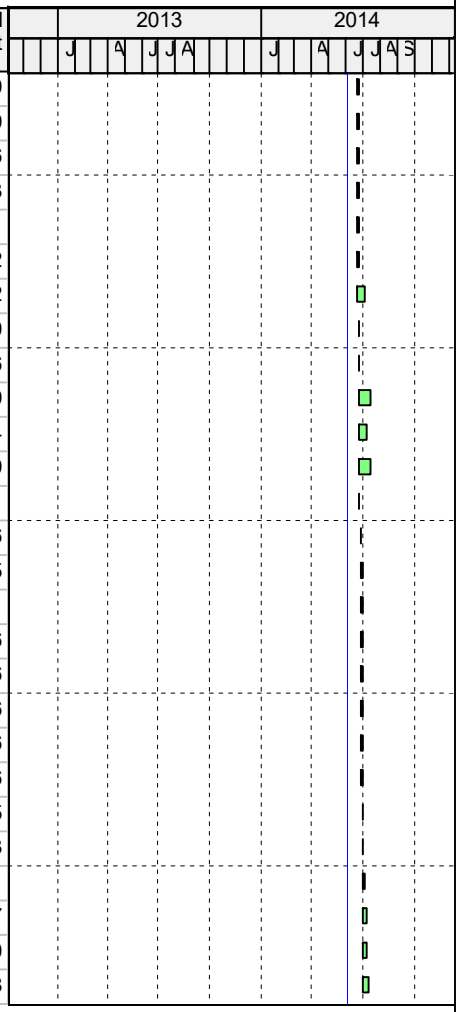



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-6018a | Install Kitchen hoods and grease ducts (OFCI) | 10 | 10 | 02-Jul-14 | 16-Jul-14 | 22 |
| MPP-1000 | Podium - West Elevation Grid X-FF Metal Panels | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 72 |
| L15-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 07-Jul-14 | 08-Jul-14 | 104 |
| L14-6040 | Test Heat Pumps - L11, L12 and L14 | 3 | 3 | 07-Jul-14 | 09-Jul-14 | 35 |
| L14-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 07-Jul-14 | 07-Jul-14 | 41 |
| L15-6036 | Framing Around Heat Pump & Soffit | 3 | 3 | 07-Jul-14 | 09-Jul-14 | 12 |
| L1B-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 10 | 07-Jul-14 | 18-Jul-14 | 20 |
| MPP-1010 | Podium - North Elevation Metal Panels | 5 | 5 | 09-Jul-14 | 15-Jul-14 | 94 |
| L16-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 10-Jul-14 | 11-Jul-14 | 23 |
| L16-6036 | Framing Around Heat Pump & Soffit | 3 | 3 | 10-Jul-14 | 14-Jul-14 | 21 |
| L15-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 10-Jul-14 | 10-Jul-14 | 12 |
| MPP-1002 | Podium - South Elevation Grid 18-15 Metal Panels | 2 | 2 | 11-Jul-14 | 14-Jul-14 | 72 |
| L17-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 15 |
| L17-6040 | Test Heat Pumps - L15, L16 and L17 | 3 | 3 | 15-Jul-14 | 17-Jul-14 | 10 |
| L17-6036 | Framing Around Heat Pump & Soffit | 3 | 3 | 15-Jul-14 | 17-Jul-14 | 13 |
| L16-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 15-Jul-14 | 15-Jul-14 | 21 |
| MPP-1004 | Podium - South Elevation Grid 13-1 Metal Panels | 4 | 4 | 15-Jul-14 | 18-Jul-14 | 72 |
| MPT-1002 | Tower - Complete West Elevation Metal Panels | 10 | 10 | 16-Jul-14 | 29-Jul-14 | 59 |
| MPT-1010 | Tower - East Elevation Gris S-A Metal Panels | 10 | 10 | 16-Jul-14 | 29-Jul-14 | 59 |
| L17-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 18-Jul-14 | 18-Jul-14 | 13 |
| MPP-1006 | Podium and Ballroom - South Elevation Metal Panels | 10 | 10 | 21-Jul-14 | 01-Aug-14 | 72 |
| L03-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 23-Jul-14 | 30-Jul-14 | 5 |
| L04-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 23-Jul-14 | 30-Jul-14 | 5 |
| LL1-Z4-8090 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 23-Jul-14 | 30-Jul-14 | 23 |
| MPT-1004 | Tower - South Elevation Grid 18-10 Metal Panels | 20 | 20 | 30-Jul-14 | 26-Aug-14 | 59 |
| MPT-1012 | Tower - North Elevation Grid 8-18 Metal Panels | 25 | 25 | 30-Jul-14 | 03-Sep-14 | 59 |
| L03-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 31-Jul-14 | 31-Jul-14 | 34 |

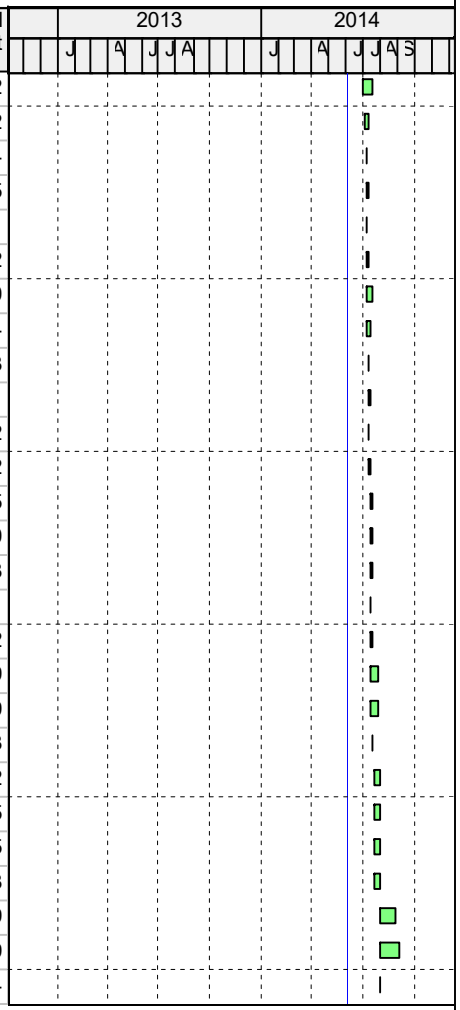



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 31-Jul-14 | 31-Jul-14 | 34 |
| LL1-Z4-8092 | Frame Ceilings/Furred Wall at Elevator Fronts | 1 | 1 | 31-Jul-14 | 31-Jul-14 | 23 |
| L05-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 31-Jul-14 | 07-Aug-14 | 5 |
| L06-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 31-Jul-14 | 07-Aug-14 | 5 |
| L03-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 01-Aug-14 | 01-Aug-14 | 35 |
| L04-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 01-Aug-14 | 01-Aug-14 | 35 |
| LL1-Z4-8094 | Electrical Rough-In at Elevator Fronts/Ceiling | 1 | 1 | 01-Aug-14 | 01-Aug-14 | 23 |
| L02-5102 | L2 - Storefront Frames | 3 | 3 | 01-Aug-14 | 05-Aug-14 | 8 |
| L03-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 35 |
| L04-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 35 |
| LL1-Z4-8096 | Fire Sprinkler Rough-in at Elevatgor Fronts/Ceiling | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 23 |
| MPL4-1000 | Upper L4 Ballroom - South Elevation Vertical Metal P: | 3 | 3 | 04-Aug-14 | 06-Aug-14 | 72 |
| L03-8405 | Cover Inspection | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 35 |
| L04-8405 | Cover Inspection | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 35 |
| LL1-Z4-8098 | Cover Inspection | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 23 |
| LL1-Z4-8100 | Insulation | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 23 |
| L03-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 35 |
| L04-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 35 |
| L02-5104 | L2 - Storefront Glazing | 2 | 2 | 06-Aug-14 | 07-Aug-14 | 8 |
| LL1-Z4-8102 | GWB Hang | 2 | 2 | 07-Aug-14 | 08-Aug-14 | 23 |
| LL1-Z5-8100 | Insulation | 1 | 1 | 07-Aug-14 | 07-Aug-14 | 26 |
| MPL4-1002 | Upper L4 Ballroom - West Elevation Vertical Metal Pa | 3 | 3 | 07-Aug-14 | 11-Aug-14 | 72 |
| LL1-Z6-8100 | Insulation | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 32 |
| L05-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 29 |
| L06-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 44 |
| L07-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 08-Aug-14 | 15-Aug-14 | 5 |
| L08-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 08-Aug-14 | 15-Aug-14 | 5 |

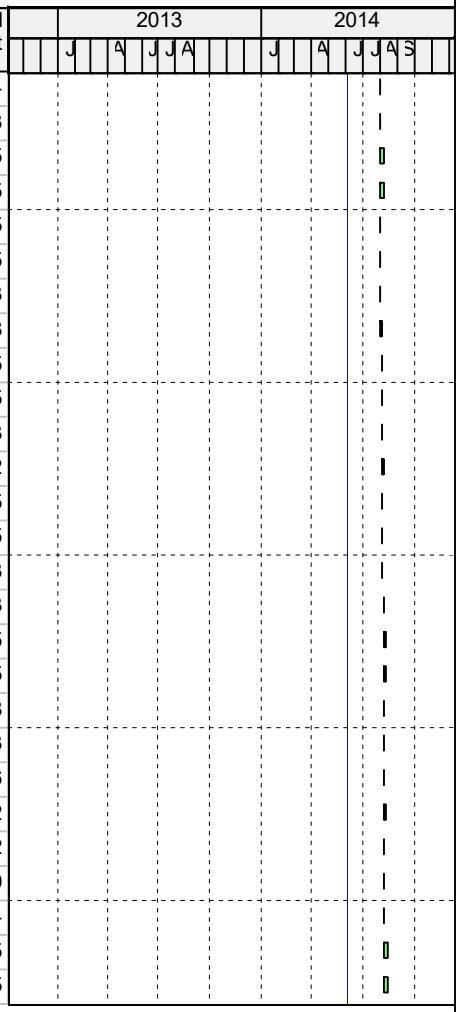



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z4-8215 | GWB Tape | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 23 |
| LL1-Z5-8102 | GWB Hang | 3 | 3 | 11-Aug-14 | 13-Aug-14 | 25 |
| LL1-Z7-8100 | Insulation | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 34 |
| L05-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 29 |
| L06-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 45 |
| L05-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 29 |
| L06-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 45 |
| MPL4-1004 | Upper L4 Ballroom - North Elevation Vertical Metal Pa | 3 | 3 | 12-Aug-14 | 14-Aug-14 | 72 |
| L03-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 35 |
| L04-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 35 |
| L05-8405 | Cover Inspection | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 29 |
| L06-8405 | Cover Inspection | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 45 |
| LL1-Z6-8102 | GWB Hang | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 29 |
| L03-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 35 |
| L04-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 35 |
| L05-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 29 |
| L06-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 45 |
| LL1-Z7-8102 | GWB Hang | 3 | 3 | 15-Aug-14 | 19-Aug-14 | 31 |
| I-1102 | Additional work at new L17 guest rooms | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 10 |
| L03-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 15-Aug-14 | 18-Aug-14 | 35 |
| L04-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 15-Aug-14 | 18-Aug-14 | 35 |
| LL1-Z4-8104 | Prime Paint | 2 | 2 | 18-Aug-14 | 19-Aug-14 | 47 |
| LL1-Z5-8215 | GWB Tape | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 23 |
| L07-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 18-Aug-14 | 18-Aug-14 | 39 |
| L08-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 18-Aug-14 | 18-Aug-14 | 38 |
| L09-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 18-Aug-14 | 25-Aug-14 | 5 |
| L10-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 18-Aug-14 | 25-Aug-14 | 5 |

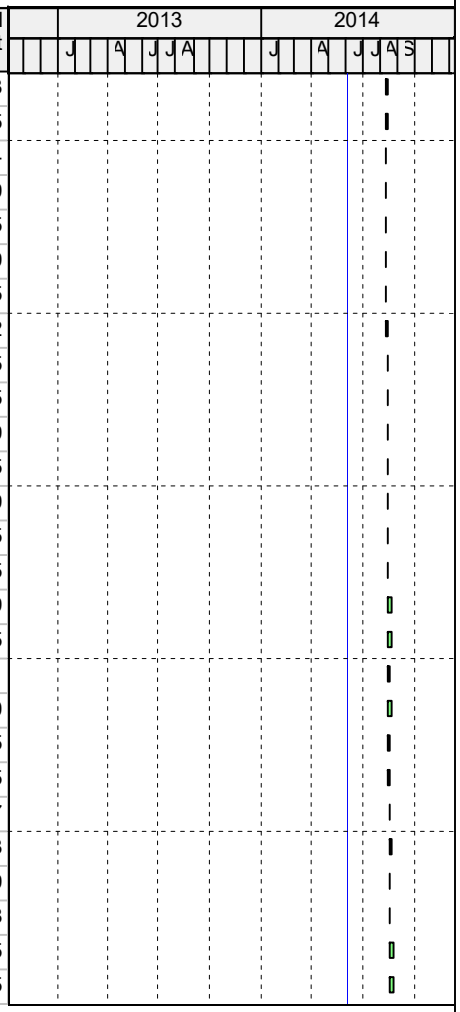



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 35 |
| L04-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 35 |
| L07-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 39 |
| L08-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 39 |
| LL1-Z4-8114 | T Bar Grid Ceiling | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 47 |
| L03-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 35 |
| L04-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 35 |
| L07-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 39 |
| L08-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 39 |
| L1RR-8100 | Insulation | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 19 |
| L1BOH1-8100 | Insulation | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 26 |
| LL1-Z4-8116 | Finish Carpentry / Millwork | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 47 |
| L03-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 35 |
| L04-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 35 |
| L05-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 29 |
| L06-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 45 |
| L07-8405 | Cover Inspection | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 39 |
| L08-8405 | Cover Inspection | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 39 |
| L03-8418 | Flooring at Elevator Lobby | 2 | 2 | 22-Aug-14 | 25-Aug-14 | 51 |
| L04-8418 | Flooring at Elevator Lobby | 2 | 2 | 22-Aug-14 | 25-Aug-14 | 51 |
| L05-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 29 |
| L06-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 45 |
| L07-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 39 |
| L08-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 39 |
| L03-8612 | L3 Pool - GWB hang/tape/finish | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 31 |
| L1BOH2-8100 | Insulation | 2 | 2 | 25-Aug-14 | 26-Aug-14 | 15 |
| LL1-Z4-8200 | First Coat Finish Paint | 2 | 2 | 25-Aug-14 | 26-Aug-14 | 47 |

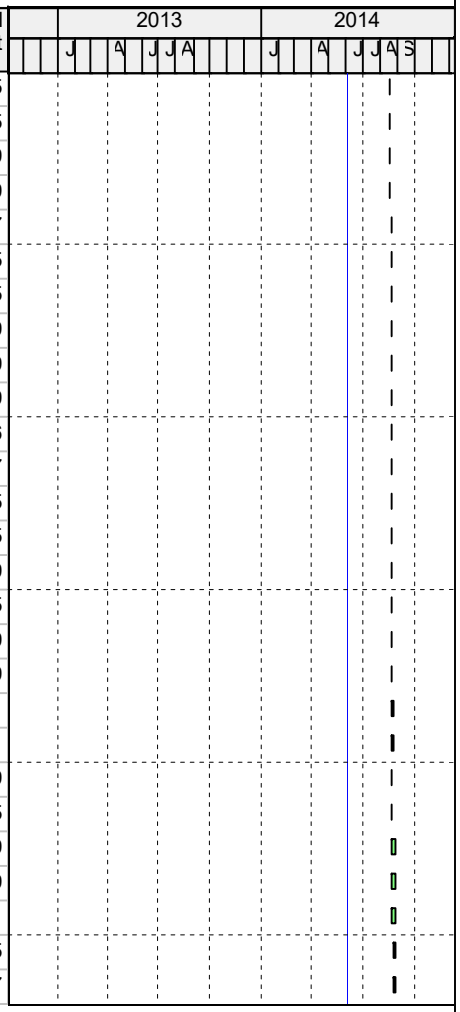



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z5-8104 | Prime Paint | 2 | 2 | 25-Aug-14 | 26-Aug-14 | 40 |
| LL1-Z6-8215 | GWB Tape | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 23 |
| L05-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 25-Aug-14 | 26-Aug-14 | 29 |
| L06-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 25-Aug-14 | 26-Aug-14 | 45 |
| LL1-Z2-8108 | Install Junior Balllroom ceiling feature (allowance) | 10 | 10 | 25-Aug-14 | 08-Sep-14 | 31 |
| LL1-Z3-8340 | Install walk-in cooler/freezer (BY OTHERS) | 5 | 5 | 25-Aug-14* | 29-Aug-14 | 24 |
| L09-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 33 |
| L10-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 32 |
| L11-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 26-Aug-14 | 03-Sep-14 | 5 |
| L12-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 26-Aug-14 | 03-Sep-14 | 5 |
| LL1-Z4-8124 | Flooring | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 47 |
| LL1-Z5-8114 | T Bar Grid Ceiling | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 40 |
| L1BOH2-8102 | GWB Hang | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 15 |
| L1RR-8102 | GWB Hang | 3 | 3 | 27-Aug-14 | 29-Aug-14 | 17 |
| L05-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 27-Aug-14 | 27-Aug-14 | 29 |
| L06-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 27-Aug-14 | 27-Aug-14 | 45 |
| L09-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 27-Aug-14 | 27-Aug-14 | 33 |
| L10-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 27-Aug-14 | 27-Aug-14 | 33 |
| MPT-1008 | Tower - South Elevation Grid 10-8 Metal Panels | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 59 |
| L05-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 29 |
| L06-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 45 |
| L09-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 33 |
| L10-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 33 |
| LL1-Z5-8116 | Finish Carpentry / Millwork | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 40 |
| LL1-Z4-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 1 | 1 | 29-Aug-14 | 29-Aug-14 | 49 |
| LL1-Z4-8126 | Doors & Hardware | 1 | 1 | 29-Aug-14 | 29-Aug-14 | 47 |
| L1BOH1-8102 | GWB Hang | 3 | 3 | 29-Aug-14 | 03-Sep-14 | 22 |

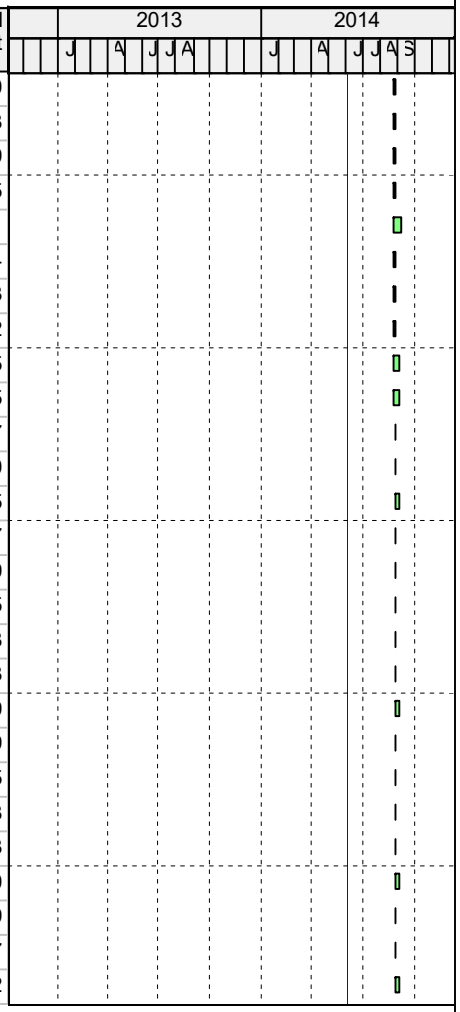



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 29-Aug-14 | 29-Aug-14 | 29 |
| L06-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 29-Aug-14 | 29-Aug-14 | 45 |
| L07-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 29-Aug-14 | 29-Aug-14 | 39 |
| L08-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 29-Aug-14 | 29-Aug-14 | 39 |
| L09-8405 | Cover Inspection | 1 | 1 | 29-Aug-14 | 29-Aug-14 | 33 |
| L10-8405 | Cover Inspection | 1 | 1 | 29-Aug-14 | 29-Aug-14 | 33 |
| L03-8614 | L3 Pool - Paint/wall finishes | 3 | 3 | 29-Aug-14 | 03-Sep-14 | 46 |
| L03-8618 | L3 Pool - Ceramic tile | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 44 |
| LL1-Z6-8104 | Prime Paint | 2 | 2 | 02-Sep-14 | 03-Sep-14 | 28 |
| LL1-Z7-8215 | GWB Tape | 5 | 5 | 02-Sep-14 | 08-Sep-14 | 23 |
| LL1-Z4-8106 | Wallcoverings | 2 | 2 | 02-Sep-14 | 03-Sep-14 | 48 |
| LL1-Z4-8201 | Final Coat Finish Paint | 2 | 2 | 02-Sep-14 | 03-Sep-14 | 47 |
| L05-8418 | Flooring at Elevator Lobby | 2 | 2 | 02-Sep-14 | 03-Sep-14 | 45 |
| L06-8418 | Flooring at Elevator Lobby | 2 | 2 | 02-Sep-14 | 03-Sep-14 | 45 |
| L07-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 02-Sep-14 | 02-Sep-14 | 39 |
| L08-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 02-Sep-14 | 02-Sep-14 | 39 |
| L09-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 02-Sep-14 | 08-Sep-14 | 33 |
| L10-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 02-Sep-14 | 08-Sep-14 | 33 |
| LL2E-8340 | LL2 - Install walk-in cooler/freezer (BY OTHERS) | 5 | 5 | 02-Sep-14 | 08-Sep-14 | 24 |
| LL1-Z3-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 02-Sep-14* | 03-Sep-14 | 49 |
| LL1-Z5-8200 | First Coat Finish Paint | 2 | 2 | 03-Sep-14 | 04-Sep-14 | 40 |
| L07-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 03-Sep-14 | 04-Sep-14 | 39 |
| L08-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 03-Sep-14 | 04-Sep-14 | 39 |
| LL1-Z6-8114 | T Bar Grid Ceiling | 1 | 1 | 04-Sep-14 | 04-Sep-14 | 28 |
| LL1-Z4-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 04-Sep-14 | 05-Sep-14 | 47 |
| LL1-Z4-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 04-Sep-14 | 05-Sep-14 | 48 |
| LL1-Z4-8204 | Mech Trim / Finish (HVAC) | 2 | 2 | 04-Sep-14 | 05-Sep-14 | 48 |

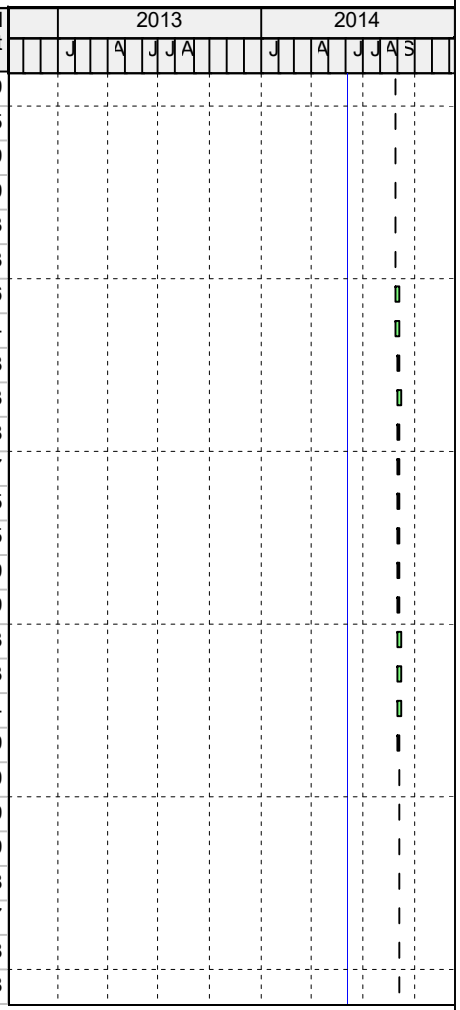



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1BOH2-8215 | GWB Tape | 7 | 7 | 04-Sep-14 | 12-Sep-14 | 15 |
| L11-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 04-Sep-14 | 04-Sep-14 | 27 |
| L12-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 04-Sep-14 | 04-Sep-14 | 26 |
| L14-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 04-Sep-14 | 11-Sep-14 | 5 |
| L15-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 04-Sep-14 | 11-Sep-14 | 5 |
| LL1-Z5-8124 | Flooring | 3 | 3 | 05-Sep-14 | 09-Sep-14 | 40 |
| LL1-Z6-8116 | Finish Carpentry / Millwork | 2 | 2 | 05-Sep-14 | 08-Sep-14 | 28 |
| L1RR-8215 | GWB Tape | 5 | 5 | 05-Sep-14 | 11-Sep-14 | 14 |
| L07-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 05-Sep-14 | 05-Sep-14 | 39 |
| L08-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 05-Sep-14 | 05-Sep-14 | 39 |
| L11-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 05-Sep-14 | 05-Sep-14 | 27 |
| L12-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 05-Sep-14 | 05-Sep-14 | 27 |
| LL1-Z3-8140a | Acoustical Ceiling Tile (remainder) | 2 | 2 | 05-Sep-14 | 08-Sep-14 | 46 |
| L07-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 39 |
| L08-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 39 |
| L11-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 27 |
| L12-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 27 |
| LL1-Z4-8140a | Acoustical Ceiling Tile (remainder) | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 48 |
| L03-8620 | L3 Pool - Plumbing Fixtures & Trim / Finish | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 44 |
| L03-8622 | L3 Pool - HVAC trim / Finish | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 44 |
| L03-8624 | L3 Pool - Fire Sprinkler Trim / Finish | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 44 |
| L03-8626 | L3 Pool - Elec Trim/ Finish | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 44 |
| L03-8628 | L3 Pool - Elec Specialties Trim / Finish | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 44 |
| LL1-Z6-8200 | First Coat Finish Paint | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 28 |
| LL1-Z7-8104 | Prime Paint | 3 | 3 | 09-Sep-14 | 11-Sep-14 | 23 |
| LL1-Z4-8134 | Pre-Clean | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 48 |
| L07-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 39 |

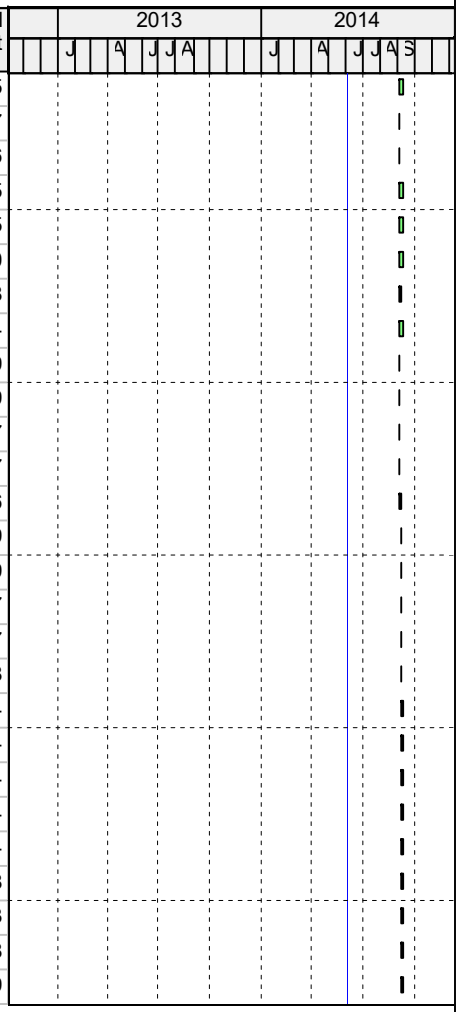



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 39 |
| L09-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 33 |
| L10-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 33 |
| LL2E-8342 | LL2 - Final connections at walk-in cooler/freezer | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 45 |
| L11-8405 | Cover Inspection | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 27 |
| L12-8405 | Cover Inspection | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 27 |
| LL1-Z5-8140 | Acoutical Ceiling Tile | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 42 |
| LL1-Z5-8126 | Doors & Hardware | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 40 |
| LL1-Z4-8132 | Contractor Pre-Punchlist | 3 | 3 | 10-Sep-14 | 12-Sep-14 | 48 |
| L1BOH1-8215 | GWB Tape | 6 | 6 | 10-Sep-14 | 17-Sep-14 | 18 |
| L07-8418 | Flooring at Elevator Lobby | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 39 |
| L08-8418 | Flooring at Elevator Lobby | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 39 |
| L09-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 33 |
| L10-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 33 |
| L11-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 10-Sep-14 | 16-Sep-14 | 27 |
| L12-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 10-Sep-14 | 16-Sep-14 | 27 |
| L1K-8340 | Install walk-in cooler/freezer (BY OTHERS0 | 10 | 10 | 10-Sep-14 | 23-Sep-14 | 23 |
| LL1-Z6-8124 | Flooring | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 28 |
| LL1-Z5-8106 | Wallcoverings | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 40 |
| LL1-Z5-8201 | Final Coat Finish Paint | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 40 |
| L09-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 33 |
| L10-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 33 |
| LL1-Z7-8114 | T Bar Grid Ceiling | 3 | 3 | 12-Sep-14 | 16-Sep-14 | 23 |
| L1RR-8104 | Prime Paint | 2 | 2 | 12-Sep-14 | 15-Sep-14 | 14 |
| L14-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 12-Sep-14 | 12-Sep-14 | 21 |
| L15-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 12-Sep-14 | 12-Sep-14 | 5 |
| L16-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 12-Sep-14 | 19-Sep-14 | 8 |

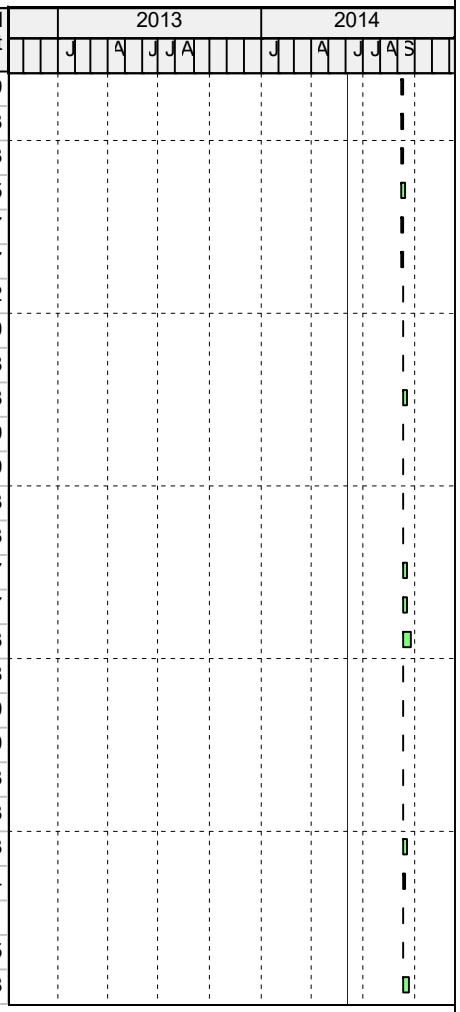



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 12-Sep-14 | 19-Sep-14 | 8 |
| LL1-Z5-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 40 |
| LL1-Z5-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 40 |
| LL1-Z5-8204 | Mech Trim / Finish (HVAC & Plumbing) | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 40 |
| LL1-Z6-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 39 |
| LL1-Z6-8126 | Doors & Hardware | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 28 |
| LL1-Z4-8210 | Owner Walk / Create Punchlist | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 48 |
| L1BOH2-8104 | Prime Paint | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 15 |
| I-3102 | Ballroom ceilings - additional work per ASIs 18, 25 | 10 | 10 | 15-Sep-14 | 26-Sep-14 | 3 |
| L09-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 33 |
| L10-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 33 |
| L14-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 21 |
| L15-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 5 |
| LL1-Z5-8203 | Install mirrors (by others) | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 40 |
| L1B-8120 | Install operable partitions | 10 | 10 | 15-Sep-14 | 26-Sep-14 | 8 |
| L03-8630 | L3 Pool - Doors & Hardware | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 44 |
| LL1-Z6-8106 | Wallcoverings | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 28 |
| LL1-Z6-8201 | Final Coat Finish Paint | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 28 |
| LL1-Z4-8212 | Final Punchlist | 3 | 3 | 16-Sep-14 | 18-Sep-14 | 48 |
| L1RR-8114 | T Bar Grid Ceiling | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 14 |
| L09-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 33 |
| L10-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 33 |
| L14-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 21 |
| L15-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 5 |
| LL1-Z7-8116 | Finish Carpentry / Millwork | 3 | 3 | 17-Sep-14 | 19-Sep-14 | 23 |
| LL1-Z5-8134 | Pre-Clean | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 40 |
| LL1-Z4-8208 | Final Clean | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 48 |

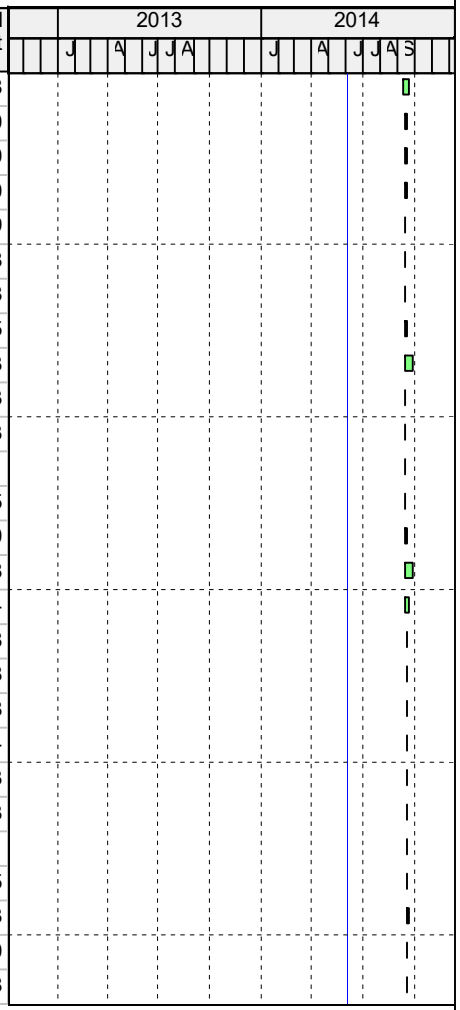



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1BOH2-8114 | T Bar Grid Ceiling | 3 | 3 | 17-Sep-14 | 19-Sep-14 | 15 |
| L09-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 33 |
| L10-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 33 |
| L11-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 27 |
| L12-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 27 |
| L14-8405 | Cover Inspection | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 21 |
| L15-8405 | Cover Inspection | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 5 |
| LL1-Z6-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 18-Sep-14 | 19-Sep-14 | 37 |
| LL1-Z6-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 18-Sep-14 | 19-Sep-14 | 36 |
| LL1-Z6-8204 | Mech Trim / Finish (HVAC & Plumbing) | 10 | 10 | 18-Sep-14 | 01-Oct-14 | 28 |
| LL1-Z5-8132 | Contractor Pre-Punchlist | 3 | 3 | 18-Sep-14 | 22-Sep-14 | 40 |
| L1BOH1-8104 | Prime Paint | 2 | 2 | 18-Sep-14 | 19-Sep-14 | 18 |
| L09-8418 | Flooring at Elevator Lobby | 2 | 2 | 18-Sep-14 | 19-Sep-14 | 33 |
| L10-8418 | Flooring at Elevator Lobby | 2 | 2 | 18-Sep-14 | 19-Sep-14 | 33 |
| L11-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 27 |
| L12-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 27 |
| L14-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 21 |
| L15-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 5 |
| LL1-Z5-8136 | Install excercise equipment (by others) | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 44 |
| LL1-Z4-8214 | LL1 Elevator Lobby / Lobby Complete | 0 | 0 | | 18-Sep-14 | 48 |
| L1RR-8116 | Finish Carpentry / Millwork | 4 | 4 | 19-Sep-14 | 24-Sep-14 | 13 |
| L11-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 27 |
| L12-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 27 |
| LL1-Z7-8200 | First Coat Finish Paint | 3 | 3 | 22-Sep-14 | 24-Sep-14 | 23 |
| L1BOH1-8114 | T Bar Grid Ceiling | 3 | 3 | 22-Sep-14 | 24-Sep-14 | 18 |
| L1BOH2-8116 | Finish Carpentry / Millwork | 3 | 3 | 22-Sep-14 | 24-Sep-14 | 15 |
| L16-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 8 |

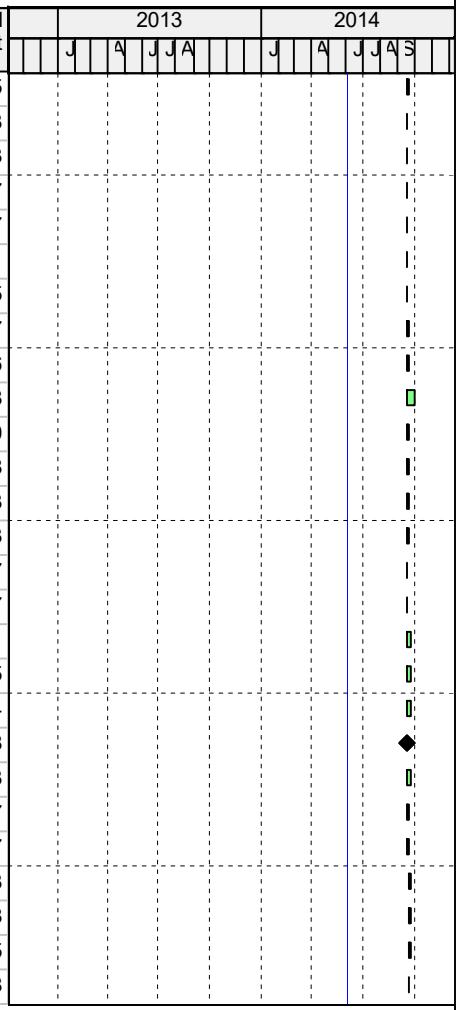



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 8 |
| L1L-8120 | Install plumbing at bar | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 5 |
| L1L-8122 | Install electrical at bar | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 5 |
| L03-8632 | L3 Pool - Install Bathroom Accessories | 3 | 3 | 22-Sep-14 | 24-Sep-14 | 44 |
| LL1-Z5-8210 | Owner Walk / Create Punchlist | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 40 |
| L11-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 27 |
| L12-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 27 |
| L16-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 8 |
| L17-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 8 |
| LL1-Z5-8212 | Final Punchlist | 3 | 3 | 24-Sep-14 | 26-Sep-14 | 40 |
| L11-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 27 |
| L12-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 27 |
| L16-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 8 |
| L17-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 8 |
| L1K-8342 | Final connections at walk-in cooler/freezer | 10 | 10 | 24-Sep-14 | 07-Oct-14 | 23 |
| LL1-Z7-8124 | Flooring | 3 | 3 | 25-Sep-14 | 29-Sep-14 | 23 |
| L1BOH1-8116 | Finish Carpentry / Millwork | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 18 |
| L1BOH2-8200 | First Coat Finish Paint | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 15 |
| L1RR-8200 | First Coat Finish Paint | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 13 |
| L11-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 25-Sep-14 | 25-Sep-14 | 27 |
| L12-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 25-Sep-14 | 25-Sep-14 | 27 |
| L14-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 25-Sep-14 | 25-Sep-14 | 21 |
| L15-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 25-Sep-14 | 25-Sep-14 | 5 |
| L16-8405 | Cover Inspection | 1 | 1 | 25-Sep-14 | 25-Sep-14 | 8 |
| L17-8405 | Cover Inspection | 1 | 1 | 25-Sep-14 | 25-Sep-14 | 8 |
| L11-8418 | Flooring at Elevator Lobby | 2 | 2 | 26-Sep-14 | 29-Sep-14 | 27 |
| L12-8418 | Flooring at Elevator Lobby | 2 | 2 | 26-Sep-14 | 29-Sep-14 | 27 |

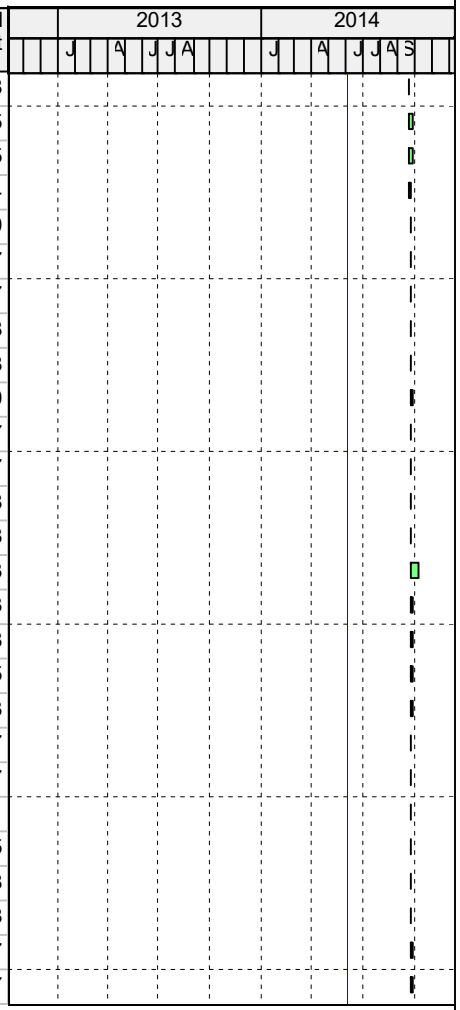



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 26-Sep-14 | 26-Sep-14 | 21 |
| L15-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 26-Sep-14 | 26-Sep-14 | 5 |
| L16-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 8 |
| L17-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 8 |
| LL1-Z5-8208 | Final Clean | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 40 |
| L1BOH1-8200 | First Coat Finish Paint | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 18 |
| L1BOH2-8124 | Flooring | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 15 |
| L1RR-8124 | Flooring | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 13 |
| L14-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 21 |
| L15-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 5 |
| LL1-Z7-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 1 | 1 | 30-Sep-14 | 30-Sep-14 | 27 |
| LL1-Z7-8126 | Doors & Hardware | 1 | 1 | 30-Sep-14 | 30-Sep-14 | 23 |
| LL1-Z5-8214 | LL1 Exercise Room Complete | 0 | 0 | | 30-Sep-14 | 40 |
| LL1-Z7-8106 | Wallcoverings | 2 | 2 | 01-Oct-14 | 02-Oct-14 | 24 |
| LL1-Z7-8201 | Final Coat Finish Paint | 3 | 3 | 01-Oct-14 | 03-Oct-14 | 23 |
| L1BOH1-8124 | Flooring | 2 | 2 | 01-Oct-14 | 02-Oct-14 | 18 |
| L14-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 01-Oct-14 | 01-Oct-14 | 21 |
| L15-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 01-Oct-14 | 01-Oct-14 | 5 |
| L14-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 21 |
| L15-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 5 |
| LL1-Z6-8140a | Acoustical Ceiling Tile (remainder) | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 28 |
| LL1-Z6-8134 | Pre-Clean | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 28 |
| L1BOH1-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 24 |
| L1BOH1-8126 | Doors & Hardware | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 18 |
| L14-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 21 |
| L15-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 5 |
| L16-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 8 |

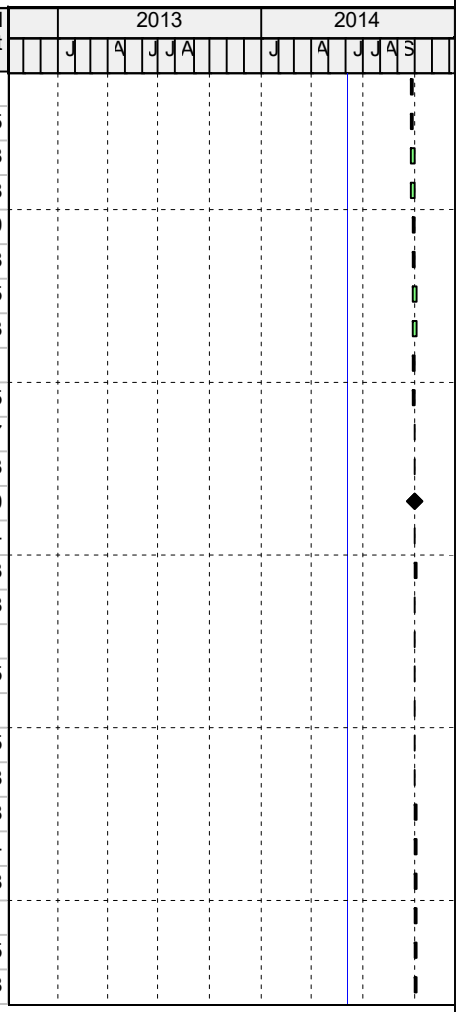



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 8 |
| LL1-Z7-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 24 |
| LL1-Z7-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 23 |
| LL1-Z7-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 23 |
| LL1-Z6-8132 | Contractor Pre-Punchlist | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 28 |
| L1BOH1-8106 | Wallcoverings | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 18 |
| L1BOH1-8201 | Final Coat Finish Paint | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 18 |
| L1BOH2-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 22 |
| L1BOH2-8126 | Doors & Hardware | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 15 |
| L1RR-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 22 |
| L1RR-8126 | Doors & Hardware | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 13 |
| I-1204 | Concierge Lounge - Additional millwork | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 1 |
| L14-8418 | Flooring at Elevator Lobby | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 21 |
| L15-8418 | Flooring at Elevator Lobby | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 21 |
| L16-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 8 |
| L17-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 8 |
| CO-7100T | CO - Preliminary Start-Up & Testing (Tower) | 10 | 10 | 06-Oct-14 | 17-Oct-14 | 5 |
| L16-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 8 |
| L17-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 8 |
| L1BOH1-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 08-Oct-14 | 09-Oct-14 | 22 |
| L1BOH1-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 08-Oct-14 | 10-Oct-14 | 20 |
| L1BOH1-8204 | Mech Trim / Finish (HVAC) | 2 | 2 | 08-Oct-14 | 09-Oct-14 | 18 |
| L1RR-8106 | Wall Coverings | 2 | 2 | 08-Oct-14 | 09-Oct-14 | 13 |
| L1RR-8201 | Final Coat Finish Paint | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 14 |
| LL1-Z6-8210 | Owner Walk / Create Punchlist | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 28 |
| L1BOH2-8106 | Wallcoverings | 2 | 2 | 09-Oct-14 | 10-Oct-14 | 15 |
| L1BOH2-8201 | Final Coat Finish Paint | 2 | 2 | 09-Oct-14 | 10-Oct-14 | 15 |

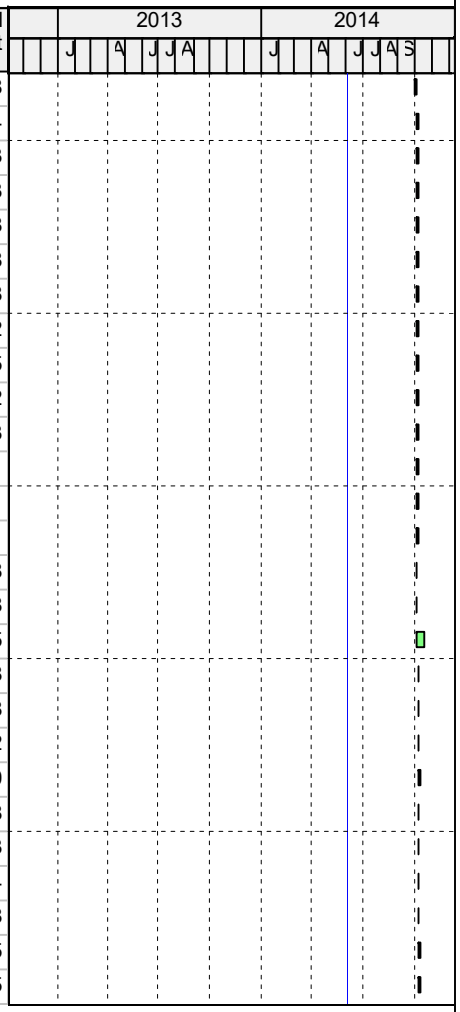



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 8 |
| L17-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 8 |
| LL1-Z7-8140a | Acoustical Ceiling Tile (remainder) | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 23 |
| LL1-Z7-8134 | Pre-Clean | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 23 |
| LL1-Z6-8212 | Final Punchlist | 3 | 3 | 10-Oct-14 | 14-Oct-14 | 28 |
| L1RR-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 10-Oct-14 | 13-Oct-14 | 20 |
| L1RR-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 10-Oct-14 | 13-Oct-14 | 19 |
| L1RR-8204 | Mech Trim / Finish (HVAC & Plumbing) | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 13 |
| L16-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 8 |
| L17-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 8 |
| LL1-8140a | Acoustical Ceiling Tile (remainder) | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 11 |
| LL1-Z2-8118a | Install decorative light fixtures | 3 | 3 | 10-Oct-14 | 14-Oct-14 | 13 |
| LL1-Z7-8132 | Contractor Pre-Punchlist | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 23 |
| L1BOH2-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 13-Oct-14 | 14-Oct-14 | 19 |
| L1BOH2-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 13-Oct-14 | 14-Oct-14 | 18 |
| L1BOH2-8204 | Mech Trim / Finish (HVAC & Plumbing) | 2 | 2 | 13-Oct-14 | 14-Oct-14 | 15 |
| L16-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 13-Oct-14 | 13-Oct-14 | 8 |
| L17-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 13-Oct-14 | 13-Oct-14 | 8 |
| L1BOH1-8140a | Acoustical Ceiling Tile (remainder) | 1 | 1 | 13-Oct-14 | 13-Oct-14 | 20 |
| L1K-8128 | Install Kitchen equipment (BY OTHERS) | 10 | 10 | 13-Oct-14 | 24-Oct-14 | 10 |
| L1BOH1-8134 | Pre-Clean | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 20 |
| L16-8418 | Flooring at Elevator Lobby | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 15 |
| L17-8418 | Flooring at Elevator Lobby | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 15 |
| LL1-Z6-8208 | Final Clean | 2 | 2 | 15-Oct-14 | 16-Oct-14 | 28 |
| L1BOH2-8140a | Acoustical Ceiling Tile (remainder) | 1 | 1 | 15-Oct-14 | 15-Oct-14 | 18 |
| LL1-Z7-8210 | Owner Walk / Create Punchlist | 1 | 1 | 16-Oct-14 | 16-Oct-14 | 23 |
| L1BOH1-8132 | Contractor Pre-Punchlist | 3 | 3 | 16-Oct-14 | 20-Oct-14 | 20 |

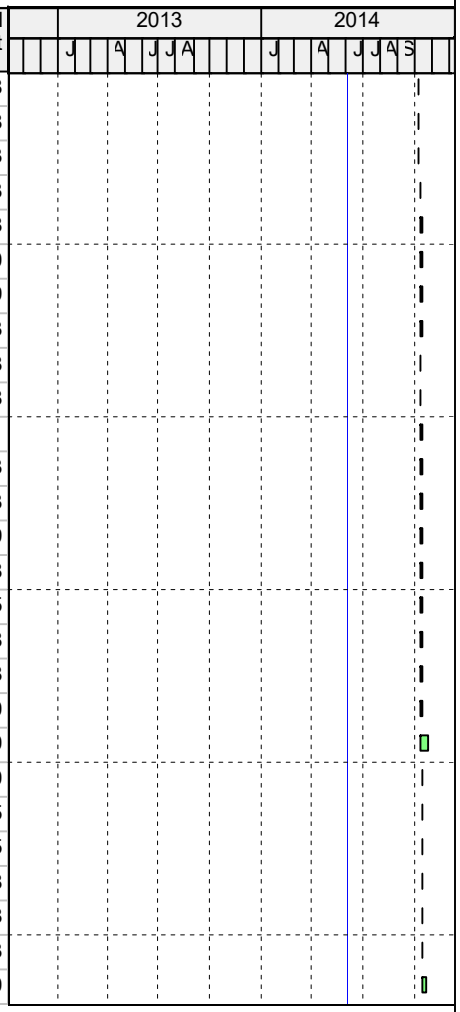



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1BOH2-8134 | Pre-Clean | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 18 |
| I-1202 | Concierge Lounge - Additional flooring work | 1 | 1 | 16-Oct-14 | 16-Oct-14 | 0 |
| LL1-Z6-8214 | LL1 - Public Restroom Complete | 0 | 0 | | 16-Oct-14 | 28 |
| LL1-Z7-8212 | Final Punchlist | 3 | 3 | 17-Oct-14 | 21-Oct-14 | 23 |
| LL1-Z2-8140a | Acoustical Ceiling Tile (remainder) | 3 | 3 | 17-Oct-14 | 21-Oct-14 | 8 |
| L1RR-8140a | Acoustical Ceiling Tile (remainder) | 1 | 1 | 17-Oct-14 | 17-Oct-14 | 16 |
| L1BOH2-8132 | Contractor Pre-Punchlist | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 18 |
| L1RR-8134 | Pre-Clean | 2 | 2 | 20-Oct-14 | 21-Oct-14 | 16 |
| CO-7102T | CO - HVAC Commissioning (Tower) | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 22 |
| CO-7110T | Fire Sprinkler Pre-Testing (Tower) | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 17 |
| CO-7116T | Fire Alarm Pre-Testing (Tower) | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 17 |
| CO-7104T | Smoke Control Pre-Testing (Tower) | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 17 |
| L1BOH1-8210 | Owner Walk / Create Punchlist | 1 | 1 | 21-Oct-14 | 21-Oct-14 | 20 |
| LL1-Z7-8208 | Final Clean | 2 | 2 | 22-Oct-14 | 23-Oct-14 | 23 |
| L1BOH1-8212 | Final Punchlist | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 20 |
| L1RR-8132 | Contrator Pre-Punchlist | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 16 |
| L1BOH2-8210 | Owner Walk / Create Punchlist | 1 | 1 | 23-Oct-14 | 23-Oct-14 | 18 |
| LL1-Z7-8214 | LL1 Back of House Complete | 0 | 0 | | 23-Oct-14 | 23 |
| L1BOH2-8212 | Final Punchlist | 3 | 3 | 24-Oct-14 | 28-Oct-14 | 18 |
| L1BOH1-8208 | Final Clean | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 20 |
| L1RR-8210 | Owner Walk / Create Punchlist | 1 | 1 | 27-Oct-14 | 27-Oct-14 | 16 |
| I-1602 | Enclosure at manlift - Framing & windows | 12 | 12 | 27-Oct-14 | 12-Nov-14 | 2 |
| L1K-8140a | Acoustical Ceiling Tile (remainder) | 3 | 3 | 27-Oct-14 | 29-Oct-14 | 7 |
| CO-7112T | City of Bellevue Fire Sprinkler Inspection / Approval (T | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 17 |
| CO-7118T | City of Bellevue Fire Alarm Inspection / Approval (Tow | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 17 |
| CO-7106T | City of Bellevue Smoke Control Testing (Tower) | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 17 |
| L1RR-8212 | Final Punchlist | 3 | 3 | 28-Oct-14 | 30-Oct-14 | 16 |

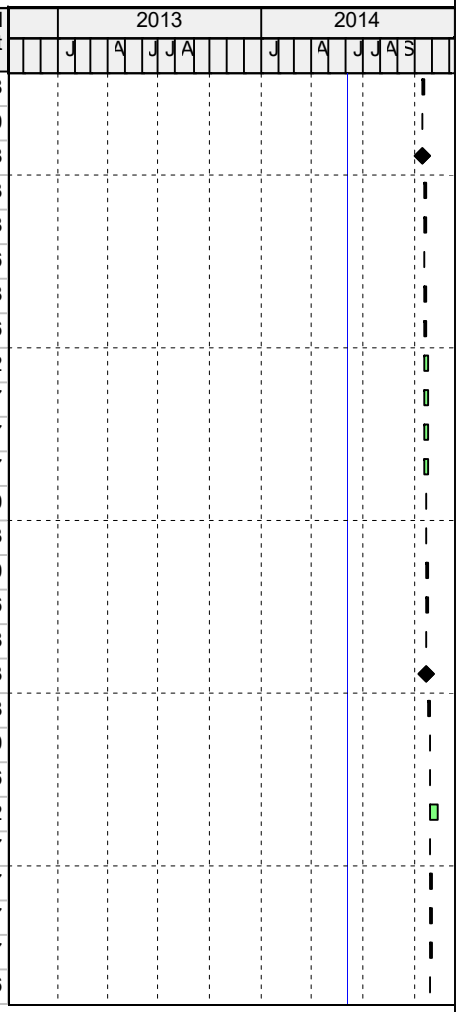



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1BOH1-8214 | L1 East Service Corridor Complete | 0 | 0 | | 28-Oct-14 | 20 |
| L1BOH2-8208 | Final Clean | 2 | 2 | 29-Oct-14 | 30-Oct-14 | 18 |
| L1B-8140a | Acoustical Ceiling Tile (remainder) | 3 | 3 | 29-Oct-14 | 31-Oct-14 | 3 |
| I-1604 | Enclosure at manlift - GWB | 12 | 12 | 30-Oct-14 | 17-Nov-14 | 2 |
| L1BOH2-81214 | L1 Back of House Complete | 0 | 0 | | 30-Oct-14 | 18 |
| L1RR-8208 | Final Clean | 2 | 2 | 31-Oct-14 | 03-Nov-14 | 16 |
| L1RR-8214 | L1 Public Restroom Complete | 0 | 0 | | 03-Nov-14 | 16 |
| I-1606 | Enclosure at manlift - Paint & finishes | 6 | 6 | 12-Nov-14 | 19-Nov-14 | 2 |
| I-1608 | Enclosure at manlift - Metal panels | 9 | 9 | 12-Nov-14 | 24-Nov-14 | 2 |
| CO-7124 | Complete Final Building Inspections | 5 | 5 | 01-Dec-14 | 05-Dec-14 | 0 |
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13 A | | |
| CM-1002 | CM - Contract Time (578 Cal Days) | 576 | 123 | 06-Mar-13 A | 05-Oct-14 | 61 |
| CM-1014 | CM - Start of Construction | 0 | 0 | 05-Apr-13 A | | |
| CM-1006 | Construction Documents Issued by Client - (Due on 7 | 0 | 0 | 05-Jun-14 | | 184 |
| CM-1008 | Finalization of Allowances - (Due on 9-2-13) | 0 | 0 | 05-Jun-14 | | 184 |
| CO-7004 | CO - Prep / Submit O&M Manuals | 40 | 40 | 25-Sep-14 | 03-Nov-14 | 32 |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 18-Oct-14 | | 7 |
| CM-1016 | CM - Owner FF+E "Build-Out" | 42 | 42 | 18-Oct-14 | 28-Nov-14 | 7 |
| CM-1018 | CM - Hotel Operations Training | 21 | 21 | 02-Nov-14* | 22-Nov-14 | 13 |
| CO-7006 | CO - Certificate of Occupancy/Substantial Completior | 0 | 0 | | 05-Dec-14 | 0 |
| CO-7122 | CO - Certificate of Occupancy | 0 | 0 | | 05-Dec-14 | 0 |
| **Misc Milestones** | | | | | | |
| CM-1020 | MM - Site Mobilization | 10 | 0 | 06-Mar-13 A | 04-Apr-13 A | |

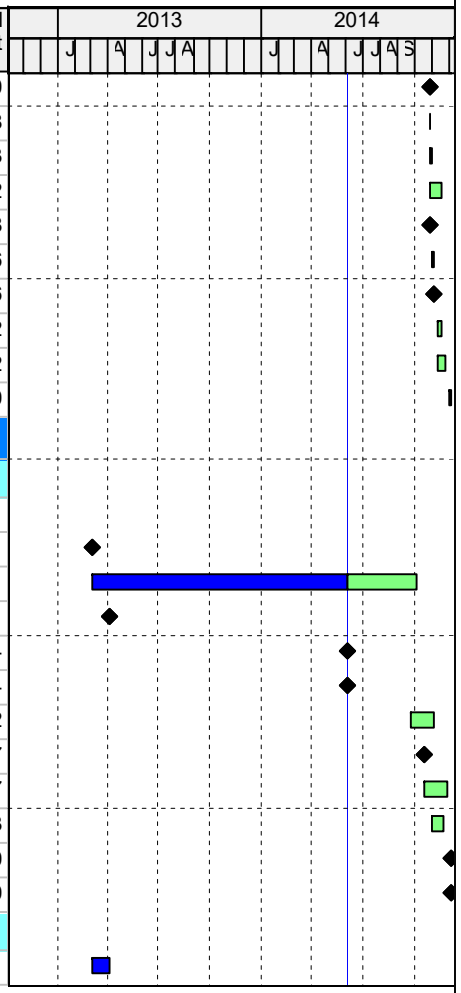



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MM-1008 | MM - Top Out - Tower / Structure | 0 | 0 | | 16-Apr-14 A | |
| MM-1004 | MM - Start Drywall In Tower | 0 | 0 | 17-Jun-14 | | 172 |
| MM-1010 | Energise Permanent Power | 5 | 5 | 29-Jun-14 | 03-Jul-14 | 124 |
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 21-Jul-14 | 90 |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| Tower Crane | | | | | | |
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 0 | 04-Jun-13 A | 14-Jun-13 A | |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 0 | 20-Jun-13 A | 24-Jun-13 A | |
| TC-5902 | Tower Crane - Erectiion | 2 | 0 | 21-Jun-13 A | 24-Jun-13 A | |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 24-Jun-13 A | | |
| TC-5906 | Tower Crane - Operatational Period | 391 | 8 | 24-Jun-13 A | 12-Jun-14 | 47 |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 1 | 13-Jun-14* | 13-Jun-14 | 32 |
| Man & Material Lifts | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 0 | 14-Jan-14 A | 20-Jan-14 A | |
| ML-5952 | Man/Material Lifts - Erect/Build Loading Dock | 5 | 0 | 21-Jan-14 A | 27-Jan-14 A | |
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 10-Feb-14 A | | |
| ML-5954 | Man/Material Lifts - Load Test / Certify | 1 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| ML-5958 | Man/Material Lifts - Operatational Period | 196 | 137 | 10-Feb-14 A | 19-Oct-14 | 2 |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 2 |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |
| Mass Excavation / Shoring | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 0 | 05-Apr-13 A | 12-Apr-13 A | |
| SW-2002 | Demolition And Utility Relocation | 8 | 0 | 15-Apr-13 A | 19-Apr-13 A | |
| SW-2010 | Grade Subgrade for Elect/Plumbing | 3 | 0 | 07-Jan-14 A | 09-Jan-14 A | |
| Site Finishes | | | | | | |

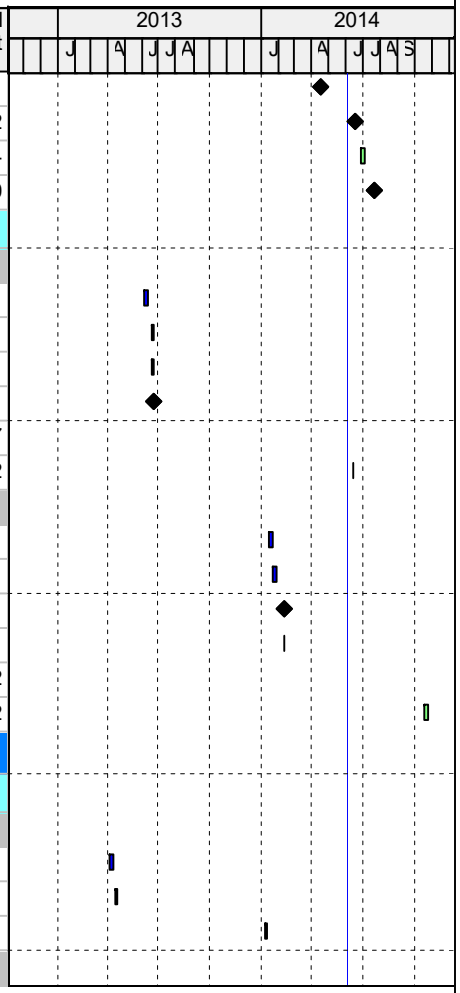



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2006 | Install Perm Power Electrical Service / Dry Utilities (Off | 15 | 3 | 20-May-14 A | 09-Jun-14 | 89 |
| SW-2004 | Offsite Water & Water Connection | 5 | 5 | 10-Jun-14 | 16-Jun-14 | 98 |
| SW-2008 | Sidewalks / Landscaping / Street Improvements | 40 | 40 | 22-Aug-14 | 17-Oct-14 | 24 |
| **Structure** | | | | | | |
| **Foundation / Substructure - (Levels LL4 / LL3)** | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 0 | 12-Jun-13 A | 27-Jun-13 A | |
| LL4-1601 | LL4 - Excavate Footings | 14 | 0 | 17-Jun-13 A | 30-Jul-13 A | |
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 0 | 18-Jun-13 A | 24-Jun-13 A | |
| LL4-1606 | LL4 - Undrgrnd Plumbing | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-1608 | LL4 - Undrgrnd Elec | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 0 | 19-Jun-13 A | 25-Jun-13 A | |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 0 | 26-Jun-13 A | 02-Aug-13 A | |
| LL4-2033 | LL4 - Shotcrete Walls | 27 | 0 | 26-Jun-13 A | 05-Aug-13 A | |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 0 | 03-Jul-13 A | 21-Aug-13 A | |
| LL4-1614 | LL4 - FRP SOG | 5 | 0 | 10-Jul-13 A | 07-Aug-13 A | |
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 0 | 12-Jul-13 A | 26-Jul-13 A | |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 0 | 13-Jul-13 A | 06-Aug-13 A | |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 0 | 22-Jul-13 A | 24-Jul-13 A | |
| LL4-1618 | LL4 - FRP Ramp SOG | 5 | 0 | 01-Aug-13 A | 07-Aug-13 A | |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2004 | LL2 - Shore / Form Deck | 8 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2006 | LL3 - M & E Inserts | 4 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2008 | LL3 - ReSteel / PT Cables | 6 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2010 | LL3 - Install Embeds | 2 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2001 | LL3 - Waterproof Walls | 3 | 0 | 05-Aug-13 A | 05-Aug-13 A | |
| LL3-2012 | LL3 - Pour / Finish Deck | 2 | 0 | 16-Aug-13 A | 16-Aug-13 A | |

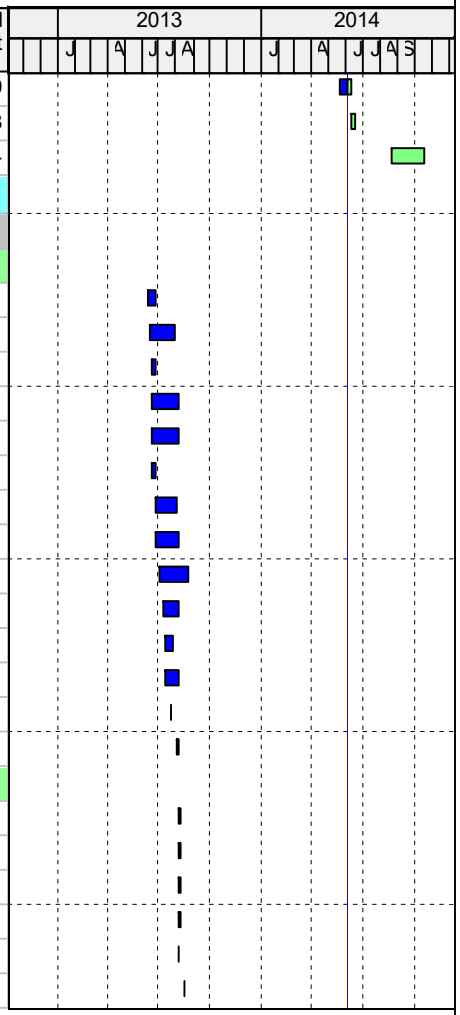


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-2014 | LL3 - Stress Tendons | 1 | 0 | 19-Aug-13 A | 19-Aug-13 A | |
| LL3-2000 | LL3 - FRP Core Walls | 8 | 0 | 19-Aug-13 A | 28-Aug-13 A | |
| LL3-2033 | LL3 - Shotcrete Walls | 5 | 0 | 23-Aug-13 A | 26-Aug-13 A | |
| LL3-2016 | LL3 - Strip / ReShore Deck | 3 | 0 | 01-Sep-13 A | 13-Sep-13 A | |
| LL3-2018 | LL3 - Remove ReShores | 4 | 0 | 04-Nov-13 A | 07-Nov-13 A | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Grids 1 to 4 - (SOG @ Loading Dock)** | | | | | | |
| LL2-2056 | LL2 - Grease Intercepter | 5 | 0 | 15-Aug-13 A | 21-Aug-13 A | |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 0 | 27-Aug-13 A | 04-Sep-13 A | |
| LL2-2027 | LL2 - Waterproof Walls | 2 | 0 | 27-Aug-13 A | 28-Aug-13 A | |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 0 | 30-Aug-13 A | 05-Sep-13 A | |
| LL2-2021 | LL2 - FRP Elec Vault | 14 | 0 | 30-Aug-13 A | 04-Sep-13 A | |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 0 | 04-Sep-13 A | 11-Sep-13 A | |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 0 | 11-Sep-13 A | 13-Sep-13 A | |
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls/Roof | 11 | 0 | 19-Sep-13 A | 03-Oct-13 A | |
| LL2-2020 | LL2 - Undrgmd Plumbing | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2022 | LL2 - Undrgmd Elec | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2031 | LL2 - FRP Generator SOG | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2015 | LL2 to LL1 FRP Columns / Misc Walls | 6 | 0 | 01-Oct-13 A | 01-Oct-13 A | |
| LL2-2029 | LL2 - F/R/P Pour #2 | 8 | 0 | 15-Jan-14 A | 24-Jan-14 A | |
| LL2-2011 | LL2 - F/R/P Pour #3 | 16 | 0 | 24-Jan-14 A | 18-Feb-14 A | |
| LL2-2019 | LL2 - F/R/P Pour #6 | 4 | 0 | 19-Feb-14 A | 17-Mar-14 A | |
| LL2-2044 | LL2 - Set Generator | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |
| LL2-2004 | LL2 - Shore / Form Deck | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |

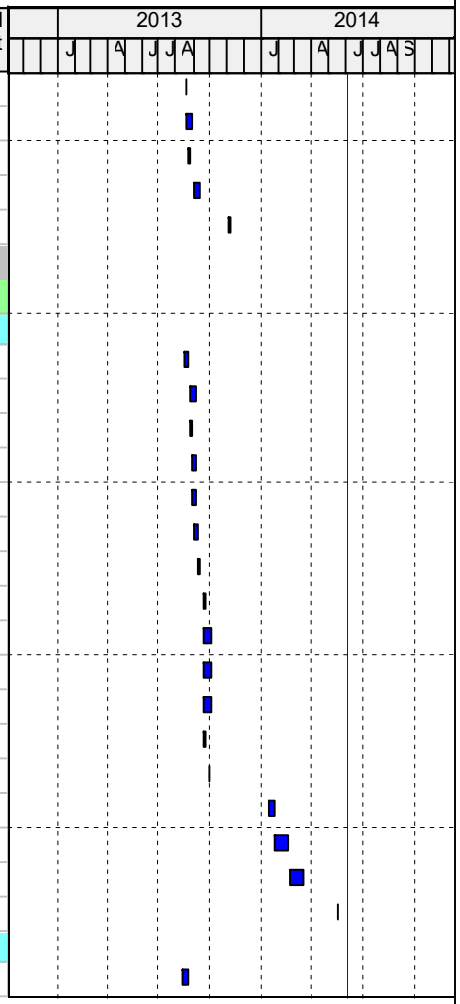



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2035 | LL2 to LL1 - Shotcrete Walls | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2006 | LL2 - M & E Inserts | 4 | 0 | 14-Aug-13 A | 19-Aug-13 A | |
| LL2-2008 | LL2 - ReSteel / PT Cables | 6 | 0 | 14-Aug-13 A | 21-Aug-13 A | |
| LL2-2010 | LL2 - Install Embeds | 3 | 0 | 14-Aug-13 A | 16-Aug-13 A | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 0 | 27-Aug-13 A | 06-Sep-13 A | |
| LL2-2012 | LL2 - Place / Finish Deck | 3 | 0 | 29-Aug-13 A | 29-Aug-13 A | |
| LL2-2023 | LL2 - Waterproof Walls | 3 | 0 | 29-Aug-13 A | 03-Sep-13 A | |
| LL2-2014 | LL2 - Stress Tendons | 1 | 0 | 30-Aug-13 A | 30-Aug-13 A | |
| LL2-2016 | LL2 - Strip / ReShore | 3 | 0 | 03-Sep-13 A | 05-Sep-13 A | |
| LL2-8234 | LL2 - Place / Finish Deck | 3 | 0 | 12-Sep-13 A | 12-Sep-13 A | |
| LL2-2000 | LL2 - FRP Core Walls | 8 | 0 | 12-Sep-13 A | 23-Sep-13 A | |
| LL2-2018 | LL2 - Remove ReShores | 4 | 0 | 13-Nov-13 A | 18-Nov-13 A | |
| LL2-2013 | LL2 - F/R/P Pour #1 | 4 | 0 | 13-Jan-14 A | 16-Jan-14 A | |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| P5A-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2000 | LL1 - FRP Core Walls | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2004 | LL1 - Shore / Form Deck | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| P6-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P6-2004 | LL1 - Shore / Form Deck | 7 | 0 | 16-Sep-13 A | 24-Sep-13 A | |
| P5A-2006 | LL1 - MEP Rough In | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2008 | LL1 - ReSteel / PT Cables | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2012 | LL1 - Place / Finish Deck | 0 | 0 | 20-Sep-13 A | | |
| P5A-2020 | LL1 - Waterproof Walls | 3 | 0 | 20-Sep-13 A | 24-Sep-13 A | |
| P5A-2014 | LL1 - Stress Tendons | 1 | 0 | 23-Sep-13 A | 23-Sep-13 A | |
| P5A-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2006 | LL1 - MEP Rough In | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |

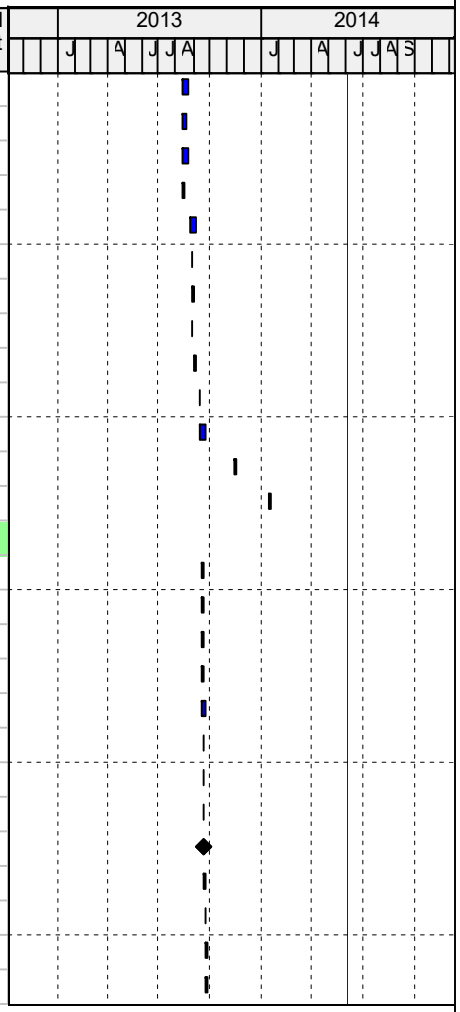



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P6-2008 | LL1 - ReSteel / PT Cables | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 24-Sep-13 A | 25-Sep-13 A | |
| P6-2020 | LL1 - Waterproof Walls | 4 | 0 | 24-Sep-13 A | 27-Sep-13 A | |
| P5A-2033 | LL1 - Resteel/Shotcrete Walls | 3 | 0 | 25-Sep-13 A | 27-Sep-13 A | |
| P5B-2002 | LL1 - FRP Columns Below | 5 | 0 | 26-Sep-13 A | 02-Oct-13 A | |
| P5B-2004 | LL1 - Shore / Form Deck | 7 | 0 | 26-Sep-13 A | 04-Oct-13 A | |
| P6-2012 | LL1 - Place / Finish Deck | 0 | 0 | 27-Sep-13 A | | |
| P6-2014 | LL1 - Stress Tendons | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2033 | LL1 - Resteel/Shotcrete Walls | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 01-Oct-13 A | 03-Oct-13 A | |
| P5B-2006 | LL1 - MEP Rough In | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2002 | FRP Columns Below | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2004 | Shore / Form Deck | 4 | 0 | 03-Oct-13 A | 08-Oct-13 A | |
| P5B-2008 | LL1 - ReSteel / PT Cables | 5 | 0 | 04-Oct-13 A | 10-Oct-13 A | |
| P5B-2010 | LL1 - Install Edgeform/Embeds | 4 | 0 | 04-Oct-13 A | 09-Oct-13 A | |
| P8-2002 | FRP Columns Below | 5 | 0 | 07-Oct-13 A | 11-Oct-13 A | |
| P8-2000 | Form/Resteel/Close Core Walls | 14 | 0 | 07-Oct-13 A | 24-Oct-13 A | |
| P8-2004 | Shore / Form Deck P8 | 8 | 0 | 07-Oct-13 A | 16-Oct-13 A | |
| P7-2002 | FRP Columns Below | 5 | 0 | 08-Oct-13 A | 14-Oct-13 A | |
| P7-2004 | Shore / Form Deck | 6 | 0 | 08-Oct-13 A | 15-Oct-13 A | |
| P10A--2006 | MEP Rough In | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2008 | ReSteel / PT Cables | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2010 | Install Edgeform/Embeds | 2 | 0 | 08-Oct-13 A | 09-Oct-13 A | |
| P5B-2012 | LL1 - Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P10A--2012 | Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P5B-2014 | LL1 - Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P7-2006 | MEP Rough In | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |

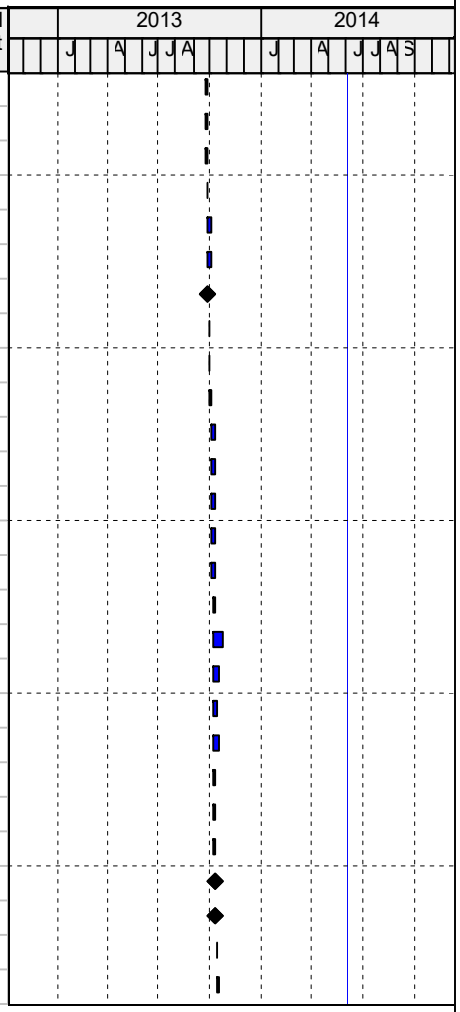



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P7-2008 | ReSteel / PT Cables | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P10A--2014 | Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P8-2020 | Shore / Form Deck P9 | 6 | 0 | 14-Oct-13 A | 21-Oct-13 A | |
| P5B-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2010 | Install Edgeform/Embeds | 2 | 0 | 15-Oct-13 A | 16-Oct-13 A | |
| P8-2006 | MEP Rough In | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2008 | ReSteel / PT Cables | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2010 | Install Edgeform/Embeds | 4 | 0 | 15-Oct-13 A | 18-Oct-13 A | |
| P10A--2016 | Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2012 | Place / Finish Deck | 0 | 0 | 18-Oct-13 A | | |
| P7-2033 | Resteel/Shotcrete Walls | 3 | 0 | 18-Oct-13 A | 22-Oct-13 A | |
| P7-2014 | Stress Tendons | 1 | 0 | 21-Oct-13 A | 21-Oct-13 A | |
| P7-2016 | Strip / ReShore Deck | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2002 | FRP Columns Below | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P10B--2000 | FRP Shear Walls Below | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2004 | Shore / Form Deck | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P8-2012 | Place / Finish Deck P 8 & 9 and Core Walls | 0 | 0 | 25-Oct-13 A | | |
| P8-2014 | Stress Tendons | 1 | 0 | 28-Oct-13 A | 28-Oct-13 A | |
| P10B--2006 | MEP Rough In | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2008 | ReSteel / PT Cables | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2010 | Install Edgeform/Embeds | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P12--2002 | FRP Columns Below | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P12--2000 | Form/Resteel/Close Core Walls | 9 | 0 | 28-Oct-13 A | 07-Nov-13 A | |
| P12--2004 | Shore / Form Deck | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P8-2016 | Strip / ReShore Deck | 3 | 0 | 29-Oct-13 A | 31-Oct-13 A | |
| P11--2002 | FRP Columns Below | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P11--2004 | Shore / Form Deck | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |

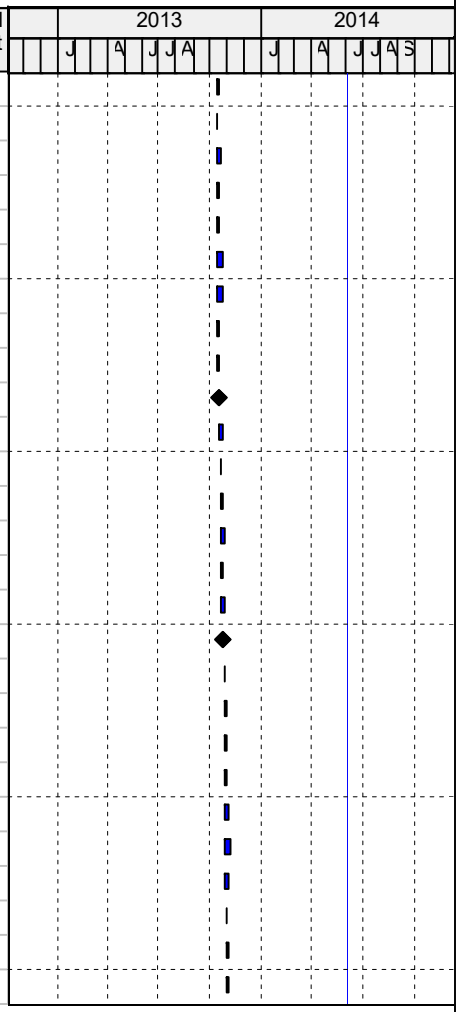



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P10B--2012 | Place / Finish Deck | 0 | 0 | 31-Oct-13 A | | |
| P10B--2014 | Stress Tendons | 1 | 0 | 01-Nov-13 A | 01-Nov-13 A | |
| P12--2006 | MEP Rough In | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12--2008 | ReSteel / PT Cables | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12--2010 | Install Edgeform/Embeds | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P10B--2016 | Strip / ReShore Deck | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2006 | MEP Rough In | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2008 | ReSteel / PT Cables | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2010 | Install Edgeform/Embeds | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2012 | Place / Finish Deck | 0 | 0 | 07-Nov-13 A | | |
| P13--2002 | FRP Columns Below | 5 | 0 | 07-Nov-13 A | 14-Nov-13 A | |
| P13--2004 | Shore / Form Deck | 9 | 0 | 07-Nov-13 A | 28-Nov-13 A | |
| P11--2014 | Stress Tendons | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| P12--2012 | Place / Finish Deck & Core Walls | 0 | 0 | 08-Nov-13 A | | |
| P11--2016 | Strip / ReShore Deck | 3 | 0 | 12-Nov-13 A | 14-Nov-13 A | |
| P12--2014 | Stress Tendons | 1 | 0 | 12-Nov-13 A | 12-Nov-13 A | |
| P14--2002 | FRP Columns Below | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P14--2000 | Form/Resteel/Close Core Walls | 8 | 0 | 19-Nov-13 A | 03-Dec-13 A | |
| P14--2004 | Shore / Form Deck | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P13A--2002 | FRP Columns Below | 5 | 0 | 21-Nov-13 A | 27-Nov-13 A | |
| P13A--2004 | Shore / Form Deck | 4 | 0 | 21-Nov-13 A | 26-Nov-13 A | |
| P13--2010 | Install Edgeform/Embeds | 5 | 0 | 22-Nov-13 A | 04-Dec-13 A | |
| P13--2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14--2006 | MEP Rough In | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14--2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14--2010 | Install Edgeform/Embeds | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P13--2006 | MEP Rough In | 5 | 0 | 26-Nov-13 A | 03-Dec-13 A | |

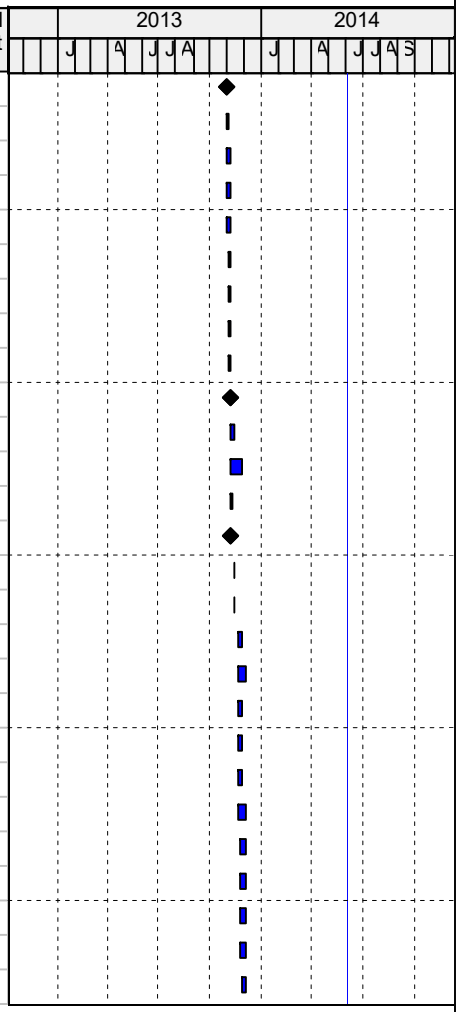



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P13A–2006 | MEP Rough In | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2008 | ReSteel / PT Cables | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2010 | Install Edgeform/Embeds | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13–2012 | Place / Finish Deck | 0 | 0 | 02-Dec-13 A | | |
| P13A–2012 | Place / Finish Deck | 0 | 0 | 03-Dec-13 A | | |
| P14–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 04-Dec-13 A | | |
| P13–2014 | Stress Tendons | 1 | 0 | 05-Dec-13 A | 05-Dec-13 A | |
| P15–2002 | FRP Columns Below | 3 | 0 | 05-Dec-13 A | 09-Dec-13 A | |
| P15–2000 | Jump/Resteel/Close Core | 9 | 0 | 05-Dec-13 A | 17-Dec-13 A | |
| P15–2004 | Shore / Form Deck | 5 | 0 | 05-Dec-13 A | 11-Dec-13 A | |
| P13–2016 | Strip / ReShore Deck | 3 | 0 | 06-Dec-13 A | 10-Dec-13 A | |
| P13A–2014 | Stress Tendons | 1 | 0 | 06-Dec-13 A | 06-Dec-13 A | |
| P14–2014 | Stress Tendons | 1 | 0 | 07-Dec-13 A | 07-Dec-13 A | |
| P15–2006 | MEP Rough In | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2008 | ReSteel / PT Cables | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2010 | Install Edgeform/Embeds | 3 | 0 | 11-Dec-13 A | 13-Dec-13 A | |
| P16-2002 | FRP Columns Below | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P16-2004 | Shore / Form Deck | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P15–2012 | Place / Finish Deck | 0 | 0 | 18-Dec-13 A | | |
| P15–2020 | Place Conc @ Core | 0 | 0 | 18-Dec-13 A | | |
| P16-2000 | Jump/Resteel/Close Core | 5 | 0 | 18-Dec-13 A | 24-Dec-13 A | |
| P16-2006 | MEP Rough In | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2008 | ReSteel / PT Cables | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2010 | Install Edgeform/Embeds | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P15–2014 | Stress Tendons | 1 | 0 | 21-Dec-13 A | 21-Dec-13 A | |
| P8-2018 | Remove Reshores | 2 | 0 | 23-Dec-13 A | 24-Dec-13 A | |
| P10A–2018 | Remove Reshores | 2 | 0 | 26-Dec-13 A | 27-Dec-13 A | |

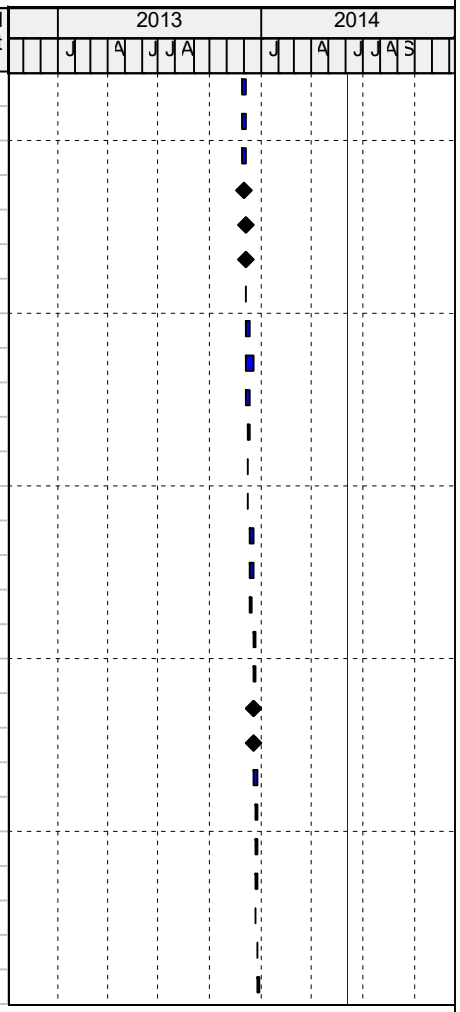



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P16-2012 | Place / Finish Deck | 0 | 0 | 26-Dec-13 A | | |
| P16-2020 | Place Conc @ Core | 0 | 0 | 26-Dec-13 A | | |
| P17-2002 | FRP Columns Below | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P17-2000 | Jump/Resteel/Close Core | 7 | 0 | 27-Dec-13 A | 07-Jan-14 A | |
| P17-2004 | Shore / Form Deck | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P10B--2018 | Remove Reshores | 2 | 0 | 30-Dec-13 A | 31-Dec-13 A | |
| P16-2014 | Stress Tendons | 1 | 0 | 31-Dec-13 A | 31-Dec-13 A | |
| P5A-2018 | LL1 - Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P11--2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P12--2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P17-2006 | MEP Rough In | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2008 | ReSteel / PT Cables | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2010 | Install Edgeform/Embeds | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P6-2018 | LL1 - Remove Reshores | 2 | 0 | 06-Jan-14 A | 07-Jan-14 A | |
| P5B-2018 | LL1 - Remove Reshores | 2 | 0 | 08-Jan-14 A | 09-Jan-14 A | |
| P17-2012 | Place / Finish Deck | 0 | 0 | 08-Jan-14 A | | |
| P17-2020 | Place Conc @ Core | 0 | 0 | 08-Jan-14 A | | |
| P18-2002 | FRP Columns Below | 5 | 0 | 09-Jan-14 A | 15-Jan-14 A | |
| P18-2000 | Jump/Resteel/Close Core | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P18-2004 | Shore / Form Deck | 3 | 0 | 09-Jan-14 A | 13-Jan-14 A | |
| LL2-2022R | MEP Rough In | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P7-2018 | Remove Reshores | 2 | 0 | 10-Jan-14 A | 13-Jan-14 A | |
| P17-2014 | Stress Tendons | 1 | 0 | 11-Jan-14 A | 11-Jan-14 A | |
| P13--2018 | Remove Reshores | 2 | 0 | 13-Jan-14 A | 14-Jan-14 A | |
| P13A--2018 | Remove Reshores | 2 | 0 | 15-Jan-14 A | 16-Jan-14 A | |
| WEA-2012 | WIND IMPACT | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| P18-2006 | MEP Rough In | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |

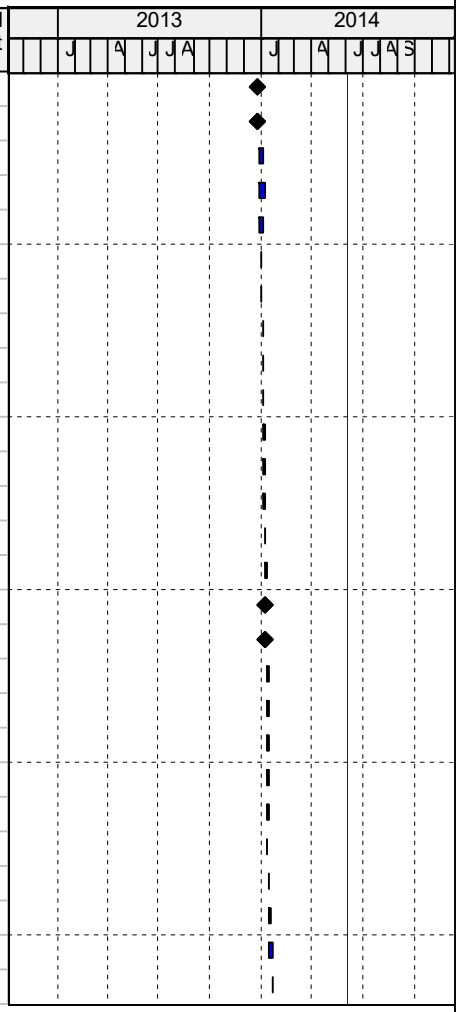


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P18-2008 | ReSteel / PT Cables | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2010 | Install Edgeform/Embeds | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2012 | Place / Finish Deck | 0 | 0 | 22-Jan-14 A | | |
| P18-2020 | Place Conc @ Core | 0 | 0 | 22-Jan-14 A | | |
| P19-2002 | FRP Columns Below | 5 | 0 | 23-Jan-14 A | 29-Jan-14 A | |
| P19-2000 | Jump/Resteel/Close Core | 4 | 0 | 23-Jan-14 A | 28-Jan-14 A | |
| P19-2004 | Shore / Form Deck | 3 | 0 | 23-Jan-14 A | 27-Jan-14 A | |
| P18-2014 | Stress Tendons | 1 | 0 | 25-Jan-14 A | 25-Jan-14 A | |
| P14–2018 | Remove Reshores | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2006 | MEP Rough In | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2008 | ReSteel / PT Cables | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2010 | Install Edgeform/Embeds | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2012 | Place / Finish Deck | 0 | 0 | 29-Jan-14 A | | |
| P19-2020 | Place Conc @ Core | 0 | 0 | 29-Jan-14 A | | |
| P20-2002 | FRP Columns Below | 5 | 0 | 30-Jan-14 A | 05-Feb-14 A | |
| P20-2000 | Jump/Resteel/Close Core | 9 | 0 | 30-Jan-14 A | 11-Feb-14 A | |
| P20-2004 | Shore / Form Deck | 6 | 0 | 30-Jan-14 A | 10-Feb-14 A | |
| P19-2014 | Stress Tendons | 1 | 0 | 01-Feb-14 A | 01-Feb-14 A | |
| P13A–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P14–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P15–2016 | Strip / ReShore Deck | 3 | 0 | 06-Feb-14 A | 10-Feb-14 A | |
| P20-2006 | MEP Rough In | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2008 | ReSteel / PT Cables | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2010 | Install Edgeform/Embeds | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| L03-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 06-Feb-14 A | 12-Feb-14 A | |
| P16-2016 | Strip / ReShore Deck | 3 | 0 | 10-Feb-14 A | 12-Feb-14 A | |
| L04-2018 | Remove Reshores | 2 | 0 | 10-Feb-14 A | 11-Feb-14 A | |

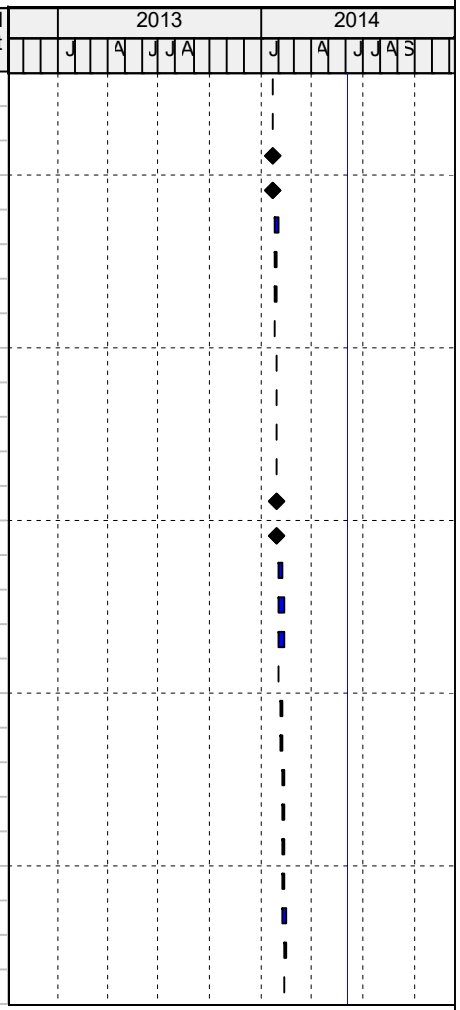



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-2018 | Remove Reshores | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| P17-2016 | Strip / ReShore Deck | 3 | 0 | 12-Feb-14 A | 14-Feb-14 A | |
| P20-2012 | Place / Finish Deck | 0 | 0 | 12-Feb-14 A | | |
| P20-2020 | Place Conc @ Core | 0 | 0 | 12-Feb-14 A | | |
| L04-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-Feb-14 A | 18-Feb-14 A | |
| P12–2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P18-2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P21-2002 | FRP Columns Below | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| P21-2000 | Jump/Resteel/Close Core | 4 | 0 | 13-Feb-14 A | 18-Feb-14 A | |
| P21-2004 | Shore / Form Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P19-2016 | Strip / ReShore Deck | 3 | 0 | 14-Feb-14 A | 18-Feb-14 A | |
| P20-2014 | Stress Tendons | 1 | 0 | 15-Feb-14 A | 15-Feb-14 A | |
| P21-2006 | MEP Rough In | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2008 | ReSteel / PT Cables | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P20-2016 | Strip / ReShore Deck | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| L05-2018 | Remove Reshores | 2 | 0 | 18-Feb-14 A | 19-Feb-14 A | |
| P21-2012 | Place / Finish Deck | 0 | 0 | 19-Feb-14 A | | |
| P21-2020 | Place Conc @ Core | 0 | 0 | 19-Feb-14 A | | |
| P22-2002 | FRP Columns Below | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P22-2000 | Jump/Resteel/Close Core | 4 | 0 | 20-Feb-14 A | 25-Feb-14 A | |
| P22-2004 | Shore / Form Deck | 3 | 0 | 20-Feb-14 A | 24-Feb-14 A | |
| L05-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P21-2014 | Stress Tendons | 1 | 0 | 22-Feb-14 A | 22-Feb-14 A | |
| P21-2016 | Strip / ReShore Deck | 3 | 0 | 24-Feb-14 A | 26-Feb-14 A | |
| P22-2006 | MEP Rough In | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2008 | ReSteel / PT Cables | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |

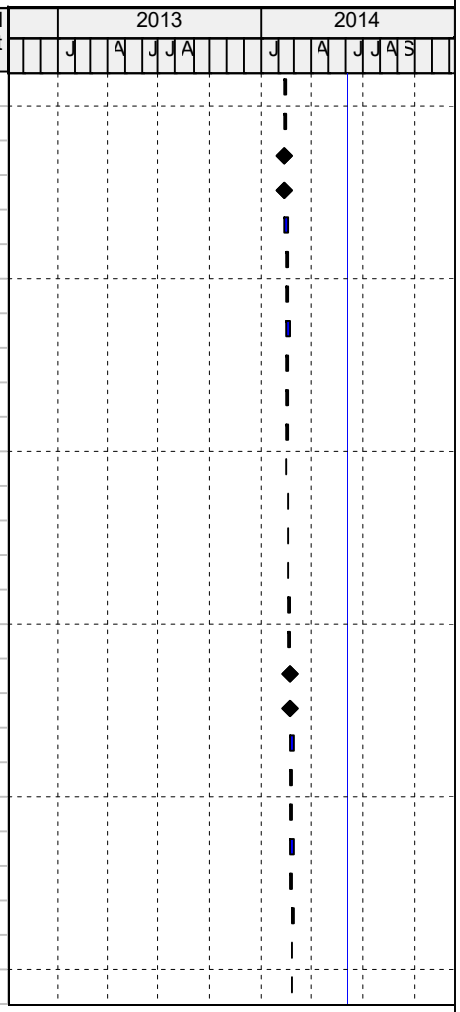



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P22-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| L06-2018 | Remove Reshores | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| P22-2012 | Place / Finish Deck | 0 | 0 | 26-Feb-14 A | | |
| P22-2020 | Place Conc @ Core | 0 | 0 | 26-Feb-14 A | | |
| P23-2002 | FRP Columns Below | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2000 | Jump/Resteel/Close Core | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2004 | Shore / Form Deck | 3 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2006 | MEP Rough In | 2 | 0 | 01-Mar-14 A | 03-Mar-14 A | |
| P22-2014 | Stress Tendons | 1 | 0 | 01-Mar-14 A | 01-Mar-14 A | |
| P23-2008 | ReSteel / PT Cables | 2 | 0 | 03-Mar-14 A | 04-Mar-14 A | |
| P22-2016 | Strip / ReShore Deck | 3 | 0 | 04-Mar-14 A | 10-Mar-14 A | |
| P23-2010 | Install Edgeform/Embeds | 2 | 0 | 04-Mar-14 A | 04-Mar-14 A | |
| L07-2018 | Remove Reshores | 2 | 0 | 04-Mar-14 A | 05-Mar-14 A | |
| P23-2012 | Place / Finish Deck | 0 | 0 | 05-Mar-14 A | | |
| P23-2020 | Place Conc @ Core | 0 | 0 | 05-Mar-14 A | | |
| P24-2002 | FRP Columns Below | 5 | 0 | 05-Mar-14 A | 07-Mar-14 A | |
| P24-2004 | Shore / Form Deck | 3 | 0 | 06-Mar-14 A | 10-Mar-14 A | |
| P24-2000 | Jump/Resteel/Close Core | 4 | 0 | 08-Mar-14 A | 10-Mar-14 A | |
| P23-2014 | Stress Tendons | 1 | 0 | 10-Mar-14 A | 10-Mar-14 A | |
| P24-2008 | ReSteel / PT Cables | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P24-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P23-2016 | Strip / ReShore Deck | 3 | 0 | 11-Mar-14 A | 17-Mar-14 A | |
| P24-2006 | MEP Rough In | 2 | 0 | 11-Mar-14 A | 11-Mar-14 A | |
| P25-2002 | FRP Columns Below | 5 | 0 | 11-Mar-14 A | 13-Mar-14 A | |
| L08-2018 | Remove Reshores | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| P24-2012 | Place / Finish Deck | 0 | 0 | 12-Mar-14 A | | |
| P24-2020 | Place Conc @ Core | 0 | 0 | 12-Mar-14 A | | |

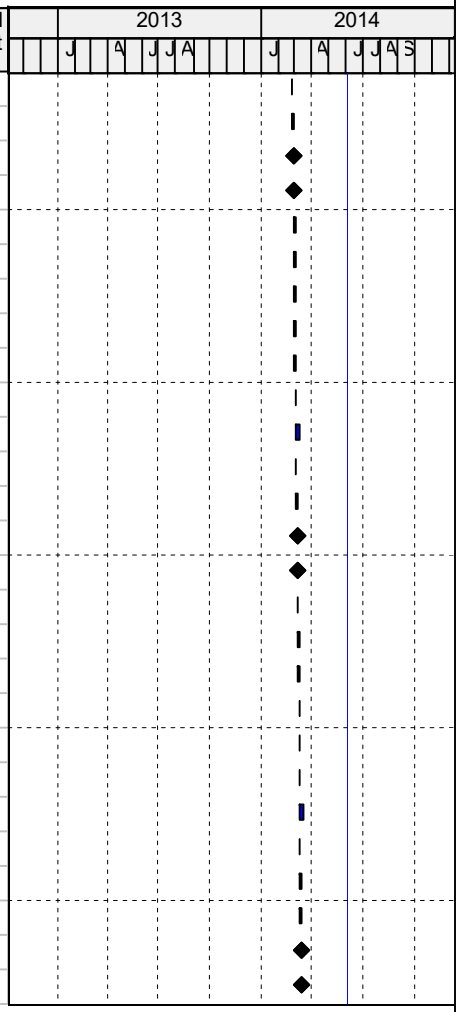


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P25-2004 | Shore / Form Deck | 3 | 0 | 13-Mar-14 A | 17-Mar-14 A | |
| P25-2000 | Jump/Resteel/Close Core | 4 | 0 | 15-Mar-14 A | 17-Mar-14 A | |
| P24-2014 | Stress Tendons | 1 | 0 | 17-Mar-14 A | 17-Mar-14 A | |
| P25-2006 | MEP Rough In | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2008 | ReSteel / PT Cables | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| L06-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 18-Mar-14 A | 20-Mar-14 A | |
| L09-2018 | Remove Reshores | 2 | 0 | 18-Mar-14 A | 19-Mar-14 A | |
| P26-2002 | FRP Columns Below | 5 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| P25-2012 | Place / Finish Deck | 0 | 0 | 19-Mar-14 A | | |
| P25-2020 | Place Conc @ Core | 0 | 0 | 19-Mar-14 A | | |
| P26-2004 | Shore / Form Deck | 3 | 0 | 20-Mar-14 A | 24-Mar-14 A | |
| L07-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 21-Mar-14 A | 25-Mar-14 A | |
| P26-2000 | Jump/Resteel/Close Core | 4 | 0 | 22-Mar-14 A | 24-Mar-14 A | |
| P26-2006 | MEP Rough In | 2 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P26-2008 | ReSteel / PT Cables | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P26-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P25-2014 | Stress Tendons | 1 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P27-2002 | FRP Columns Below | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| P26-2012 | Place / Finish Deck | 0 | 0 | 26-Mar-14 A | | |
| P26-2020 | Place Conc @ Core | 0 | 0 | 26-Mar-14 A | | |
| L08-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 26-Mar-14 A | 28-Mar-14 A | |
| L10-2018 | Remove Reshores | 2 | 0 | 26-Mar-14 A | 27-Mar-14 A | |
| P27-2004 | Shore / Form Deck | 3 | 0 | 27-Mar-14 A | 31-Mar-14 A | |
| P27-2000 | Jump/Resteel/Close Core | 4 | 0 | 29-Mar-14 A | 31-Mar-14 A | |
| P27-2006 | MEP Rough In | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2008 | ReSteel / PT Cables | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |

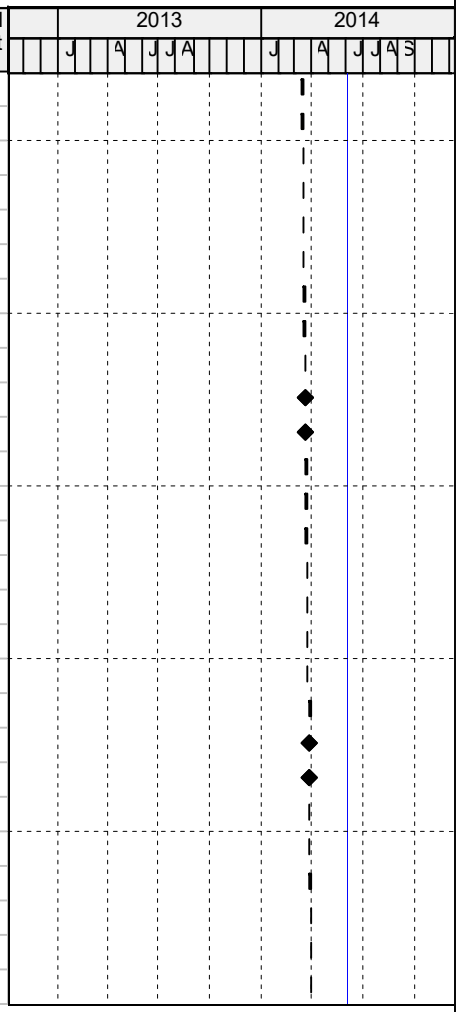



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P27-2010 | Install Edgeform/Embeds | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P26-2014 | Stress Tendons | 1 | 0 | 31-Mar-14 A | 31-Mar-14 A | |
| L09-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 31-Mar-14 A | 02-Apr-14 A | |
| P24-2016 | Strip / ReShore Deck | 3 | 0 | 01-Apr-14 A | 07-Apr-14 A | |
| L11-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 02-Apr-14 A | |
| L12-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 03-Apr-14 A | |
| P27-2012 | Place / Finish Deck | 0 | 0 | 02-Apr-14 A | | |
| P27-2020 | Place Conc @ Core | 0 | 0 | 02-Apr-14 A | | |
| P28-2002 | FRP Columns Below | 5 | 0 | 02-Apr-14 A | 04-Apr-14 A | |
| P28-2004 | Shore / Form Deck | 4 | 0 | 03-Apr-14 A | 08-Apr-14 A | |
| L10-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| P27-2014 | Stress Tendons | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| P25-2016 | Strip / ReShore Deck | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L14-2018 | Remove Reshores | 2 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| P28-2000 | Jump/Resteel/Close Core | 7 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| P28-2006 | MEP Rough In | 4 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2008 | ReSteel / PT Cables | 4 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Apr-14 A | 11-Apr-14 A | |
| L12-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| P28-2012 | Place / Finish Deck | 0 | 0 | 14-Apr-14 A | | |
| P28-2020 | Place Conc @ Core | 0 | 0 | 14-Apr-14 A | | |
| P29-2002 | FRP Columns Above Roof Deck | 3 | 0 | 14-Apr-14 A | 18-Apr-14 A | |
| P26-2016 | Strip / ReShore Deck | 3 | 0 | 14-Apr-14 A | 17-Apr-14 A | |
| L14-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-Apr-14 A | 18-Apr-14 A | |
| P28-2014 | Stress Tendons | 1 | 0 | 17-Apr-14 A | 17-Apr-14 A | |
| P29-2000 | Strip Core | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |

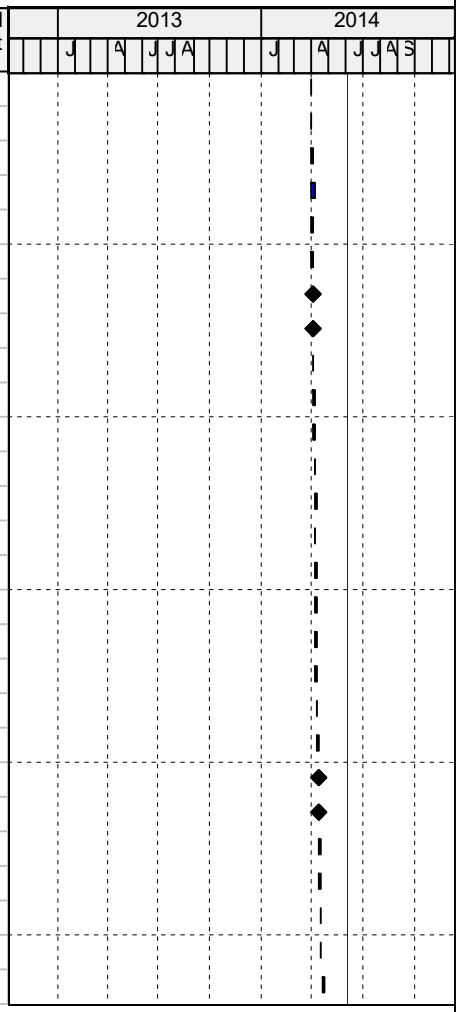



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P27-2016 | Strip / ReShore Deck | 3 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L15-2018 | Remove Reshores | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| P28-2016 | Strip / ReShore Deck | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L15-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L16-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-May-14 A | 19-May-14 A | |
| L16-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2019 | Grind Ceiling for Skim Coat | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 11 |
| **Ballroom Catwalk & Roof** | | | | | | |
| PC-2100 | Erect Structural Steel @ Porte Cochere | 3 | 0 | 30-Jan-14 A | 03-Feb-14 A | |
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 7 | 0 | 07-Feb-14 A | 17-Feb-14 A | |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| PC-2102 | Metal Decking @ Porte Cochere/ Roof | 2 | 0 | 17-Apr-14 A | 18-Apr-14 A | |
| BR-2112 | BR - Fireproofing @ Structural Steel | 2 | 0 | 27-May-14 A | 30-May-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Mech Penthouse** | | | | | | |
| PH-8706 | Set Mech Equipment @ Tower Roof | 3 | 0 | 22-May-14 A | 28-May-14 A | |
| PH-8708 | Set Equipment @ Penthouse | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| PH-8700 | PH - Structural Steel and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| **Vertical Circulation** | | | | | | |
| **Stairs** | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 25-Nov-13 A | 26-Nov-13 A | |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 27-Nov-13 A | 03-Dec-13 A | |
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 04-Dec-13 A | 05-Dec-13 A | |
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 06-Dec-13 A | 09-Dec-13 A | |
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 2 | 0 | 03-Feb-14 A | 04-Feb-14 A | |

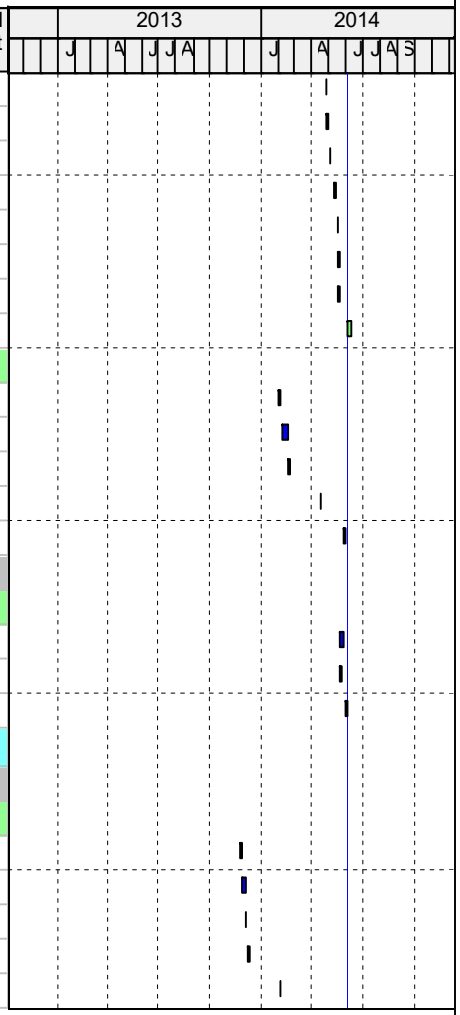


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 2 | 0 | 06-Feb-14 A | 07-Feb-14 A | |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 2 | 0 | 07-Feb-14 A | 07-Feb-14 A | |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 2 | 0 | 07-Feb-14 A | 10-Feb-14 A | |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 2 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 2 | 0 | 06-Mar-14 A | 07-Mar-14 A | |
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 2 | 0 | 07-Mar-14 A | 10-Mar-14 A | |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 2 | 0 | 13-Mar-14 A | 14-Mar-14 A | |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 2 | 0 | 08-Apr-14 A | 21-Apr-14 A | |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| S1-4040 | Stair 1 - Set Mtl Stairs / Railings L18 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 10-Dec-13 A | 11-Dec-13 A | |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 12-Dec-13 A | 13-Dec-13 A | |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 16-Dec-13 A | 17-Dec-13 A | |
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 18-Dec-13 A | 19-Dec-13 A | |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 2 | 0 | 12-Feb-14 A | 13-Feb-14 A | |
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 2 | 0 | 13-Feb-14 A | 13-Feb-14 A | |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 2 | 0 | 13-Feb-14 A | 14-Feb-14 A | |
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 2 | 0 | 19-Feb-14 A | 20-Feb-14 A | |
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 2 | 0 | 21-Feb-14 A | 24-Feb-14 A | |

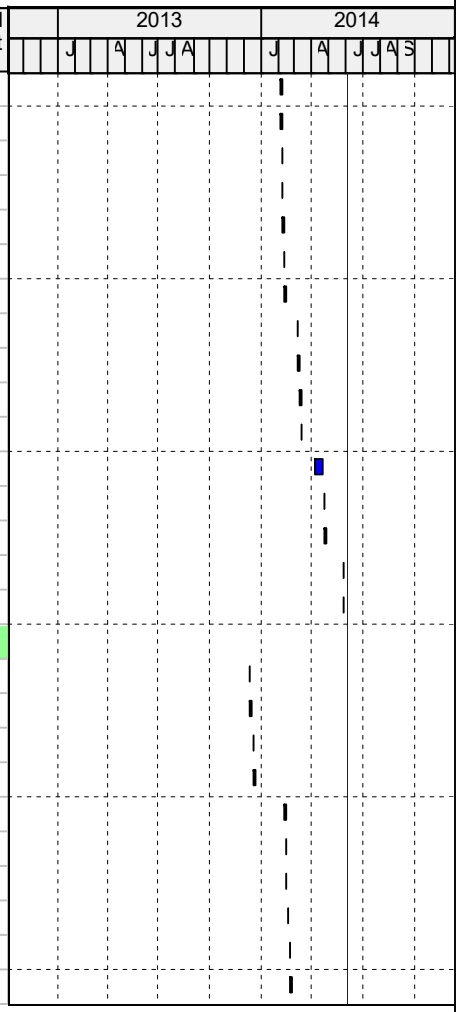



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 2 | 0 | 19-Mar-14 A | 20-Mar-14 A | |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 2 | 0 | 21-Mar-14 A | 22-Mar-14 A | |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 2 | 0 | 14-May-14 A | 15-May-14 A | |
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 2 | 0 | 16-May-14 A | 19-May-14 A | |
| S2-4038 | Stair 2 - Set Mtl Stairs / Railings L17 | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - Set Metal Stairs / Railings LL2 | 6 | 0 | 05-Mar-14 A | 20-Mar-14 A | |
| S3-4002 | Stair 3 - Set Metal Stairs / Railings LL1 | 6 | 0 | 17-Mar-14 A | 21-Mar-14 A | |
| S3-4004 | Stair 3 - Permanent Railings / Final Finishes | 4 | 4 | 05-Jun-14 | 10-Jun-14 | 113 |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |
| S4-4000 | Stair 4 - Set Metal Stairs / Railings LL2 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4002 | Stair 4 - Set Metal Stairs / Railings LL1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4004 | Stair 4 -Set Metal Stairs / Railings L1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4006 | Stair 4 - Permanent Railings / Final Finishes | 4 | 4 | 05-Jun-14 | 10-Jun-14 | 113 |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |
| S6-4000 | Stair 6 - Set Metal Stairs / Railings | 5 | 5 | 09-Jun-14 | 13-Jun-14 | 108 |
| S6-4002 | Stair 6 - Permanent Railings / Final Finishes | 2 | 2 | 16-Jun-14 | 17-Jun-14 | 108 |
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 4 | 05-Jun-14 | 10-Jun-14 | 118 |
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes | 5 | 5 | 09-Jun-14 | 13-Jun-14 | 110 |

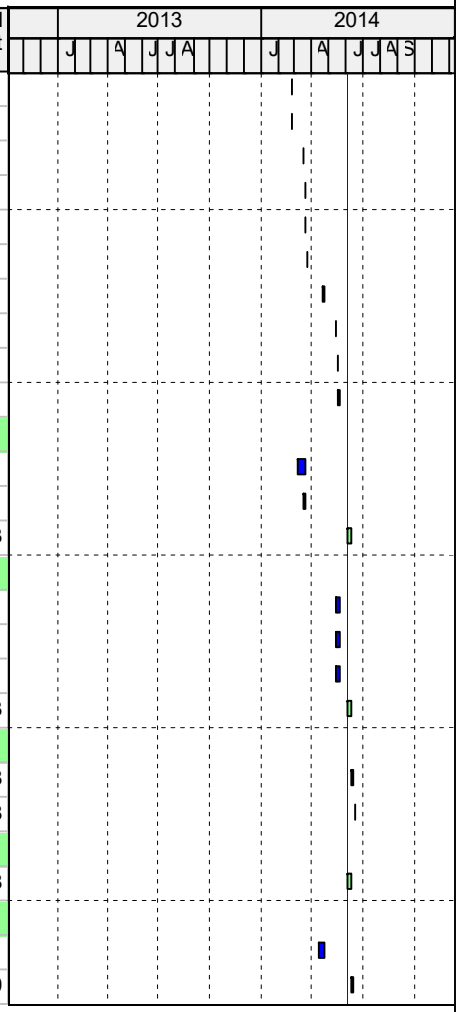



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a -Set Metal Stairs / Railings L1 | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 110 |
| S4a-4002 | Stair 4a - Permanent Railings / Final Finishes | 2 | 2 | 12-Jun-14 | 13-Jun-14 | 110 |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 07-Jun-13 A | | |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 0 | 17-Jun-13 A | 21-Jun-13 A | |
| EL-1004 | Elev - Submittal Approval | 21 | 0 | 21-Jun-13 A | 01-Jan-14 A | |
| EL-1006 | Elev - Release to Manufacturing | 14 | 0 | 02-Jan-14 A | 15-Jan-14 A | |
| EL-1008 | Elev - Fabrication (Engineered Geared) | 95 | 0 | 16-Jan-14 A | 05-Jun-14 | 34 |
| EL-1010 | Elev - Machines delivered | 1 | 0 | 12-May-14 A | 12-May-14 A | |
| EL-1011 | Elev - Elevator Machines Flown & Set At Top Of Hoist | 5 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5016 | Elev 5 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-1216 | Elev 1&2 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-3416 | Elev 3&4 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-1202 | Elev 1&2 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-3402 | Elev 3&4 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-5018 | Elev 5 - Set Hoistway Machines | 3 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| EL-1218 | Elev 1&2 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-3418 | Elev 3&4 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-1204 | Elev 1&2 - Install Rails & Brackets | 17 | 17 | 05-Jun-14 | 27-Jun-14 | 8 |
| EL-3404 | Elev 3&4 - Install Rails & Brackets | 18 | 18 | 05-Jun-14* | 30-Jun-14 | 5 |
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 12-Jun-14 | | 23 |
| EL-1200 | Elev 1&2 - Hoistway Clear & Ready (GC) | 0 | 0 | 12-Jun-14 | | 84 |
| EL-3400 | Elev 3&4 - Hoistway Clear & Ready (GC) | 0 | 0 | 12-Jun-14 | | 84 |
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 12-Jun-14 | | 84 |

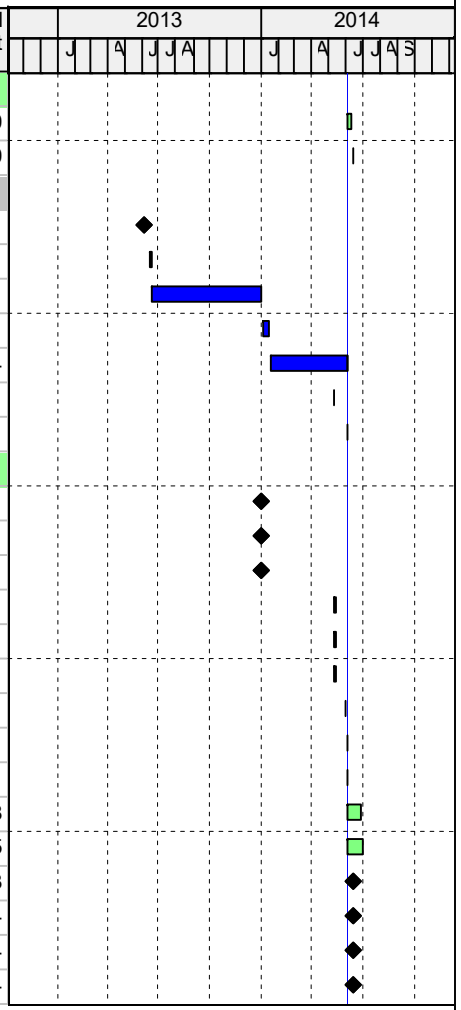


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-1206 | Elev 1&2 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 27-Jun-14 | 8 |
| EL-1207 | Elev 1&2 - Install Pit Equipment/Car Sling/CWT Fram | 3 | 3 | 30-Jun-14 | 02-Jul-14 | 8 |
| EL-3406 | Elev 3&4 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 30-Jun-14 | 5 |
| EL-3407 | Elev 3&4 - Install Pit Equipment/Car Sling/CWT Fram | 5 | 5 | 01-Jul-14 | 08-Jul-14 | 5 |
| EL-1208 | Elev 1&2 - Install MHoist & Cable | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 8 |
| EL-5004 | Elev 5 - Install Rails & Brackets | 13 | 13 | 07-Jul-14 | 23-Jul-14 | 2 |
| EL-3408 | Elev 3&4 - Install Hoist & Cable | 5 | 5 | 09-Jul-14 | 15-Jul-14 | 5 |
| EL-1210 | Elev 1&2 - Install Entrances/Doors/Fixtures/Fascia | 19 | 19 | 11-Jul-14 | 06-Aug-14 | 8 |
| EL-3410 | Elev 3&4 - Install Entrances/Doors/Fixtures/Fascia | 30 | 30 | 16-Jul-14 | 26-Aug-14 | 5 |
| EL-5006 | Elev 5 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 23-Jul-14 | 2 |
| EL-5007 | Elev 5 - Install Pit Equipment/Car Sling/CWT Frame/V | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 2 |
| EL-5008 | Elev 5 - Install MHoist & Cable | 4 | 4 | 31-Jul-14 | 05-Aug-14 | 2 |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 2 | 2 | 01-Aug-14* | 04-Aug-14 | 44 |
| EL-6018 | Elev 6 - Set Hoistway Machines | 2 | 2 | 05-Aug-14 | 06-Aug-14 | 44 |
| EL-5010 | Elev 5 - Install Entrances/Doors/Fixtures/Fascia | 21 | 21 | 06-Aug-14 | 04-Sep-14 | 2 |
| EL-6016 | Elev 6 - Hoistway Walls Complete (GC) | 0 | 0 | | 06-Aug-14 | 44 |
| EL-1212 | Elev 1&2 - Install Hoistway Equipment/Pipe & Wire | 17 | 17 | 07-Aug-14 | 29-Aug-14 | 29 |
| EL-6004 | Elev 6 - Install Cylinders/Rails & Brackets | 4 | 4 | 07-Aug-14 | 12-Aug-14 | 44 |
| EL-6006 | Elev 6 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 12-Aug-14 | 44 |
| EL-6007 | Elev 6 - Install Pit Equipment/Car Sling | 3 | 3 | 13-Aug-14 | 15-Aug-14 | 44 |
| EL-6010 | Elev 6 - Install Entrances/Doors/Fixtures/Fascia | 3 | 3 | 18-Aug-14 | 20-Aug-14 | 44 |
| EL-6012 | Elev 6 - Install Hoistway Equipment/Pipe & Wire | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 44 |
| EL-6014 | Elev 6 - Install Cab/Wiring/Door Operator(s) | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 44 |
| EL-3412 | Elev 3&4 - Install Hoistway Equipment/Pipe & Wire | 23 | 23 | 27-Aug-14 | 29-Sep-14 | 16 |
| EL-1214 | Elev 1&2 - Install Cab/Wiring/Door Operator(s) | 16 | 16 | 02-Sep-14 | 23-Sep-14 | 29 |
| EL-6022 | Elev 6 - Adjust | 5 | 5 | 02-Sep-14 | 08-Sep-14 | 44 |
| EL-5012 | Elev 5 - Install Hoistway Equipment/Pipe & Wire | 14 | 14 | 05-Sep-14 | 24-Sep-14 | 2 |

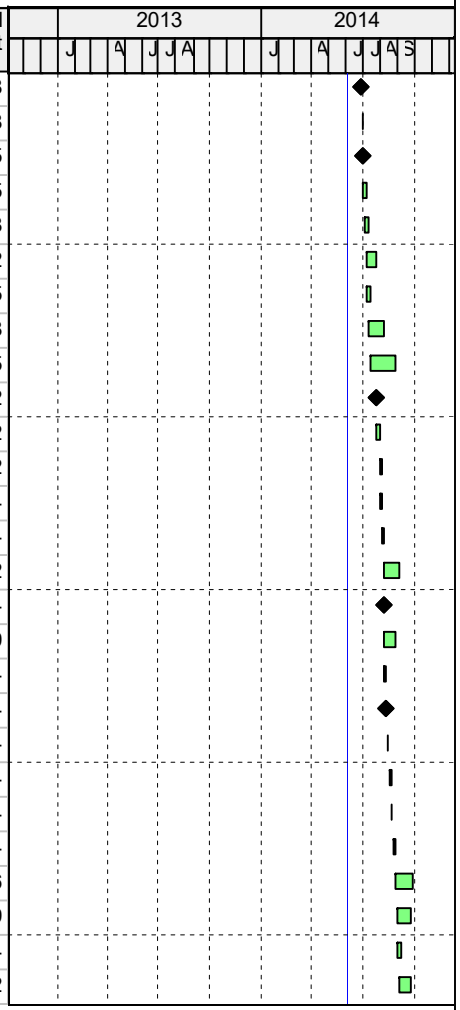


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6024 | Elev 6 - Clean / Paint / Punchlist | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 44 |
| EL-6026 | Elev 6 - Inspections | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 63 |
| EL-1222 | Elev 1&2 - Adjust | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 29 |
| EL-5014 | Elev 5 - Install Cab/Wiring/Door Operator(s) | 7 | 7 | 25-Sep-14 | 03-Oct-14 | 2 |
| EL-3414 | Elev 3&4 - Install Cab/Wiring/Door Operator(s) | 10 | 10 | 30-Sep-14 | 13-Oct-14 | 16 |
| EL-1224 | Elev 1&2 - Clean / Paint / Punchlist | 3 | 3 | 01-Oct-14 | 03-Oct-14 | 29 |
| EL-1226 | Elev 1&2 - Inspections | 2 | 2 | 04-Oct-14 | 05-Oct-14 | 43 |
| EL-5022 | Elev 5 - Adjust | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 2 |
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 2 |
| EL-3422 | Elev 3&4 - Adjust | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 16 |
| EL-5026 | Elev 5 - Inspections | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 4 |
| EL-3424 | Elev 3&4 - Clean / Paint / Punchlist | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 16 |
| EL-3426 | Elev 3&4 - Inspections | 2 | 2 | 24-Oct-14 | 25-Oct-14 | 25 |
| **Exterior Shell** | | | | | | |
| **Elevations** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2** | | | | | | |
| L3D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Feb-14 A | 12-Feb-14 A | |
| L3-5308 | L3- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 17-Feb-14 A | 21-Feb-14 A | |
| L4D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Feb-14 A | 19-Feb-14 A | |
| L4-5308 | L4- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Feb-14 A | 28-Feb-14 A | |
| L5D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Feb-14 A | 26-Feb-14 A | |
| L5-5308 | L5- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 03-Mar-14 A | 07-Mar-14 A | |
| L6D5308 | Deliver/Stock Wall Panels | 1 | 0 | 05-Mar-14 A | 05-Mar-14 A | |
| L6-5308 | L6- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L7-5308 | L7- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L7D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Mar-14 A | 12-Mar-14 A | |

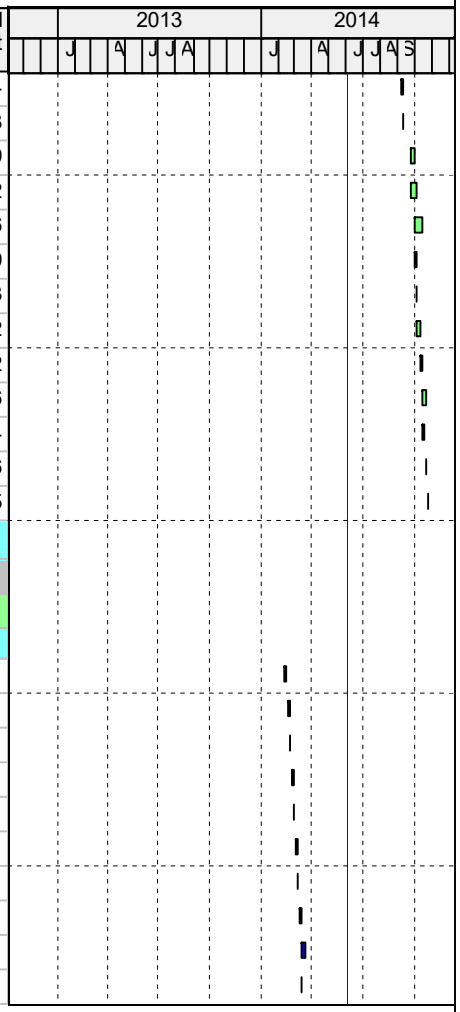



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L8D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Mar-14 A | 19-Mar-14 A | |
| L8-5308 | L8- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Mar-14 A | 28-Mar-14 A | |
| L9D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L9-5308 | L9- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 31-Mar-14 A | 07-Apr-14 A | |
| 10D5308 | Deliver/Stock Wall Panels | 1 | 0 | 02-Apr-14 A | 02-Apr-14 A | |
| L10-5308 | L10- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 07-Apr-14 A | 11-Apr-14 A | |
| 11D5308 | Deliver/Stock Wall Panels | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L11-5308 | L11- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 11-Apr-14 A | 18-Apr-14 A | |
| 12D5308 | Deliver/Stock Wall Panels | 1 | 0 | 16-Apr-14 A | 16-Apr-14 A | |
| L12-5308 | L12- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Apr-14 A | 25-Apr-14 A | |
| 14D5308 | Deliver/Stock Wall Panels | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L14-5308 | L14 - Support Frame/Sheathing for Metal Wall Panel | 5 | 0 | 24-Apr-14 A | 01-May-14 A | |
| 15D5308 | Deliver/Stock Wall Panels | 1 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L15-5308 | L15 - Support Frame/Sheathing for Metal Wall Panel | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| 16D5308 | Deliver/Stock Wall Panels | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L16-5308 | L16- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| 17D5308 | Deliver/Stock Wall Panels | 1 | 0 | 14-May-14 A | 14-May-14 A | |
| L17-5308 | L17 - Support Frame/Sheathing for Metal Wall Panel | 5 | 1 | 20-May-14 A | 05-Jun-14 | 28 |
| LL2-5308 | LL2 Thru L4 - Support Frame/Sheathing for Metal Wa | 6 | 6 | 06-Jun-14 | 13-Jun-14 | 6 |
| LL1-5308 | LL1 - Support Frame/Sheathing for Metal Wall Panel | 6 | 6 | 13-Jun-14 | 20-Jun-14 | 6 |
| L1-5308 | L1 - Support Frame/Sheathing for Metal Wall Panels | 9 | 9 | 20-Jun-14 | 02-Jul-14 | 6 |
| **Level 1** | | | | | | |
| L1-5102 | L1 - Storefront Frames | 9 | 9 | 15-Jul-14 | 25-Jul-14 | 8 |
| L1-5104 | L1 - Storefront Glazing | 4 | 4 | 28-Jul-14 | 31-Jul-14 | 8 |
| EP-5110 | L1 - Revolving Doors | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 38 |
| L3-5102 | L3- Storefront Frames | 7 | 7 | 08-Aug-14 | 18-Aug-14 | 24 |
| L3-5104 | L3 - Storefront Glazing | 3 | 3 | 19-Aug-14 | 21-Aug-14 | 24 |

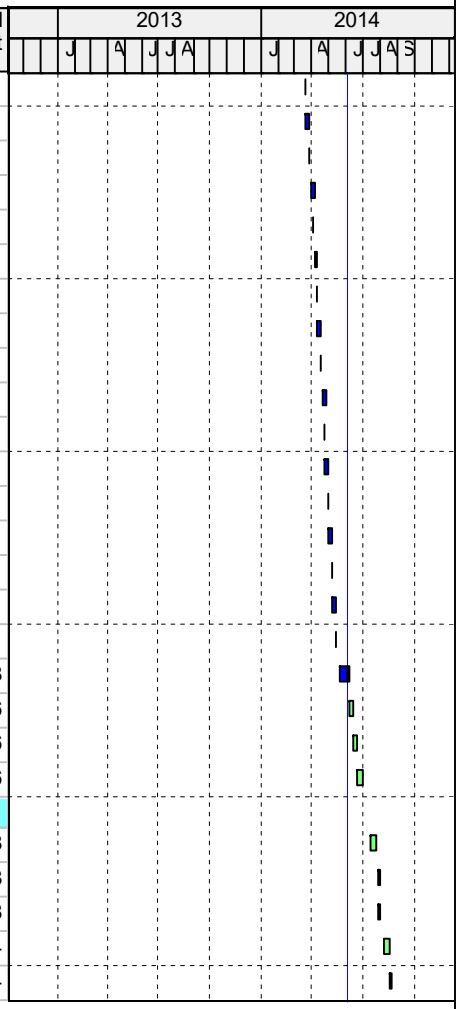


Actual Work | Remaining Work | Critical Remai... | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Levels 3-4** | | | | | | |
| L3-5130 | L3 - Install Punch Windows | 5 | 0 | 24-Feb-14 A | 10-Mar-14 A | |
| L4-5130 | L4 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 12-Mar-14 A | |
| L5-5130 | L5 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L6-5130 | L6- Install Punch Windows | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L7-5130 | L7 - Install Punch Windows | 5 | 0 | 18-Mar-14 A | 21-Mar-14 A | |
| L8-5130 | L8 - Install Punch Windows | 5 | 0 | 24-Mar-14 A | 28-Mar-14 A | |
| L9-5130 | L9 - Install Punch Windows | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L10-5130 | L10 - Install Punch Windows | 5 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-5130 | L11 - Install Punch Windows | 5 | 0 | 14-Apr-14 A | 21-Apr-14 A | |
| L12-5130 | L12 - Install Punch Windows | 5 | 0 | 22-Apr-14 A | 25-Apr-14 A | |
| L14-5130 | L14 - Install Punch Windows | 5 | 0 | 28-Apr-14 A | 05-May-14 A | |
| L15-5130 | L15 - Install Punch Windows | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| L16-5130 | L16 - Install Punch Windows | 5 | 0 | 12-May-14 A | 20-May-14 A | |
| L17-5130 | L17 - Install Punch Windows | 5 | 3 | 27-May-14 A | 10-Jun-14 | 68 |
| **Roofs** | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 49 |
| RF-4026 | L1 - City Park - Protection Board | 3 | 3 | 11-Jul-14 | 15-Jul-14 | 49 |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 49 |
| **Pool Membrane - (elev 18')** | | | | | | |
| RF-4034 | Pool Waterproofing / Membrane | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 31 |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 15 | 15 | 25-Jun-14 | 16-Jul-14 | 13 |
| RF-4010 | AR - Set Mechanical Equipment | 5 | 5 | 02-Jul-14 | 09-Jul-14 | 83 |
| RF-4012 | AR - Coping / Flashing | 4 | 4 | 02-Jul-14 | 08-Jul-14 | 99 |

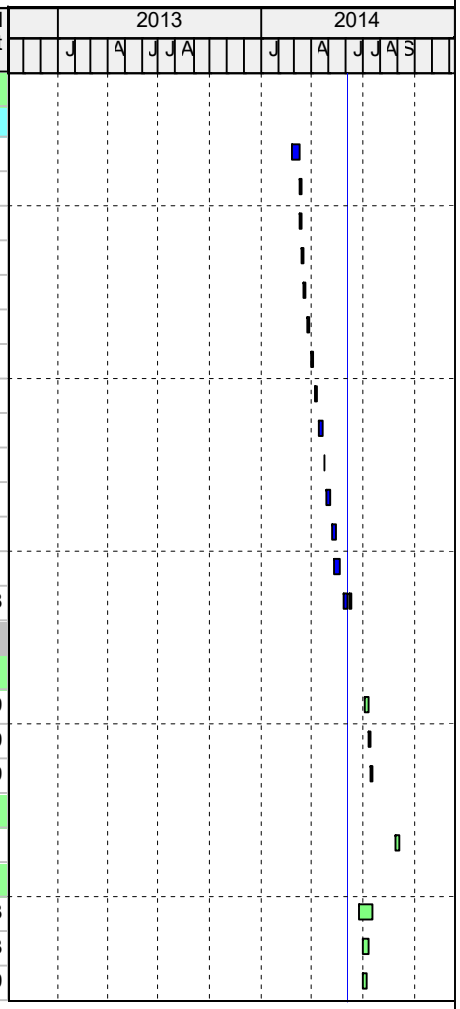


Actual Work | Remaining Work | Critical Remai... | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 25 |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |
| PC-4008 | RF - Entry / Porte Cochere Roofing System | 6 | 6 | 18-Jun-14 | 25-Jun-14 | 13 |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | RF - Upper Ballroom Roofing System | 3 | 3 | 10-Jun-14 | 12-Jun-14 | 9 |
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 4 | 4 | 13-Jun-14 | 18-Jun-14 | 13 |
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |
| RF-4018 | TR - Terrace Roof - Roofing System | 5 | 5 | 10-Jul-14 | 16-Jul-14 | 85 |
| RF-4020 | TR - Terrace Roof - Coping / Flashing | 3 | 3 | 17-Jul-14 | 21-Jul-14 | 90 |
| RF-4022 | TR - Terrace Roof - Glass Railing | 5 | 5 | 17-Jul-14 | 23-Jul-14 | 85 |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Perimeter Framing / Sul | 10 | 2 | 02-Jun-14 A | 06-Jun-14 | 11 |
| RF-4002 | Tower Roof - Roofing System | 8 | 2 | 03-Jun-14 A | 10-Jun-14 | 9 |
| **PH - Roof - (elev 173')** | | | | | | |
| RF-4030 | PH - Roofing System | 8 | 8 | 09-Jun-14 | 18-Jun-14 | 9 |
| RF-4032 | PH - Coping / Flashing | 3 | 3 | 19-Jun-14 | 23-Jun-14 | 101 |
| **Rough-In's** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6002 | LL4 - Layout | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| LL4-6008 | LL4 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL4-6012 | LL4 - Fire Sprinkler RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6014 | LL4 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6018 | LL4 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6004 | LL4 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |

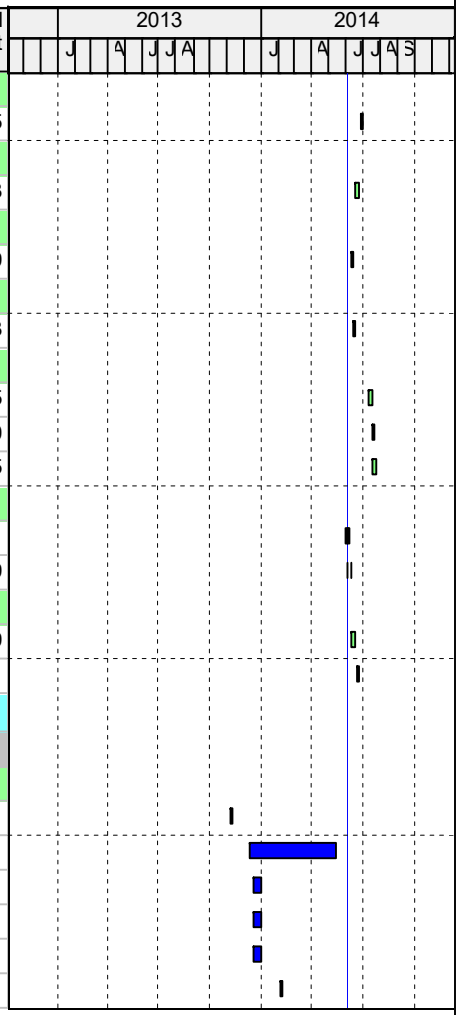



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-6010 | LL4 - Elevator pits | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| LL4-6016 | LL4 - Electrical RI | 10 | 10 | 09-Jun-14 | 20-Jun-14 | 39 |
| LL4-6020 | LL4 - H Mtl Frames | 3 | 3 | 09-Jun-14 | 11-Jun-14 | 46 |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties RI | 8 | 8 | 09-Jun-14 | 18-Jun-14 | 41 |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 2 | 08-Jul-14 | 09-Jul-14 | 27 |
| LL4-6024 | LL4 - Inspections | 2 | 2 | 10-Jul-14 | 11-Jul-14 | 27 |
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6002 | LL3 - Layout | 1 | 0 | 19-Nov-13 A | 19-Nov-13 A | |
| LL3-6008 | LL3 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL3-6012 | LL3 - Fire Sprinkler RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6014 | LL3 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6018 | LL3 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6004 | LL3 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL3-6020 | LL3 - H Mtl Frames | 3 | 0 | 08-May-14 A | 09-May-14 A | |
| LL3-6010 | LL3 - F/P Curbs | 5 | 0 | 19-May-14 A | 19-May-14 A | |
| LL3-6016 | LL3 - Electrical RI | 10 | 10 | 09-Jun-14 | 20-Jun-14 | 42 |
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties RI | 8 | 8 | 09-Jun-14 | 18-Jun-14 | 44 |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 2 | 08-Jul-14 | 09-Jul-14 | 30 |
| LL3-6024 | LL3 - Inspections | 2 | 2 | 10-Jul-14 | 11-Jul-14 | 30 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6002 | LL2 - Layout | 1 | 0 | 14-Jan-14 A | 14-Jan-14 A | |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| LL2-6012 | LL2 - Fire Sprinkler RI | 10 | 0 | 21-Jan-14 A | 03-Feb-14 A | |
| LL2-6014 | LL2 - Plumbing RI | 10 | 0 | 21-Jan-14 A | 14-Feb-14 A | |
| LL2E-6016 | LL2 - Electrical RI | 8 | 0 | 03-Feb-14 A | 17-Mar-14 A | |
| LL2-6016 | LL2 - Electrical RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2-6018 | LL2 - HVAC RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |

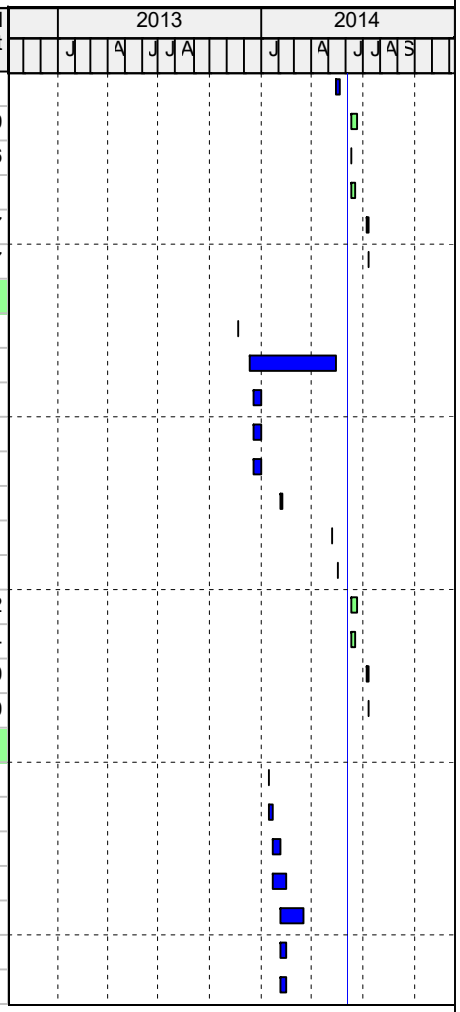



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2–6004 | LL2 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL2E-6004 | LL2 - CMU Walls | 10 | 0 | 04-Mar-14 A | 09-May-14 A | |
| LL2E-6012 | LL2 - Fire Sprinkler RI | 8 | 0 | 21-Mar-14 A | 01-Apr-14 A | |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 24-Apr-14 A | |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 3 | 1 | 23-Apr-14 A | 05-Jun-14 | 6 |
| LL2E-6020 | LL2 - H Mtl Frames | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| LL2-6020 | LL2 - H Mtl Frames | 3 | 0 | 12-May-14 A | 13-May-14 A | |
| LL2E-6008 | LL2 - Int Wall Framing | 5 | 4 | 13-May-14 A | 12-Jun-14 | 41 |
| LL2E-6014 | LL2 - Plumbing RI | 8 | 4 | 13-May-14 A | 18-Jun-14 | 41 |
| LL2E-6018 | LL2 - HVAC RI | 8 | 4 | 13-May-14 A | 08-Jul-14 | 38 |
| LL2E-6022 | LL2 - Fire Alarm / Elec Specialties RI | 8 | 4 | 13-May-14 A | 18-Jun-14 | 51 |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties RI | 8 | 8 | 19-May-14 A | 18-Jun-14 | 46 |
| LL2-6015 | LL2 - Main Elect Room Set Equip / RI - Power to Ma | 15 | 15 | 13-Jun-14 | 03-Jul-14 | 86 |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 4 | 10-Jul-14 | 15-Jul-14 | 28 |
| LL2-6024 | LL2 - Inspections | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 28 |
| LL2-6010 | LL2 - F/P Curbs @ Parking | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 49 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6002 | Layout | 3 | 0 | 03-Jan-14 A | 08-Jan-14 A | |
| LL1-6008 | Int Wall Framing & Inspection | 6 | 2 | 08-Jan-14 A | 06-Jun-14 | 8 |
| LL1-Z2-6002 | Layout | 3 | 0 | 08-Jan-14 A | 14-Jan-14 A | |
| LL1-Z3-6002 | Layout | 3 | 0 | 14-Jan-14 A | 17-Jan-14 A | |
| LL1-Z2-6008 | Int Wall Framing & Inspection | 6 | 0 | 17-Jan-14 A | 07-Apr-14 A | |
| LL1-Z3-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-Jan-14 A | 04-Feb-14 A | |
| LL1-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 09-May-14 A | |
| LL1-Z2-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 28-Apr-14 A | |
| LL1-Z3-6004 | CMU Walls (At All Areas North of Q-Line) | 3 | 0 | 03-Feb-14 A | 13-May-14 A | |

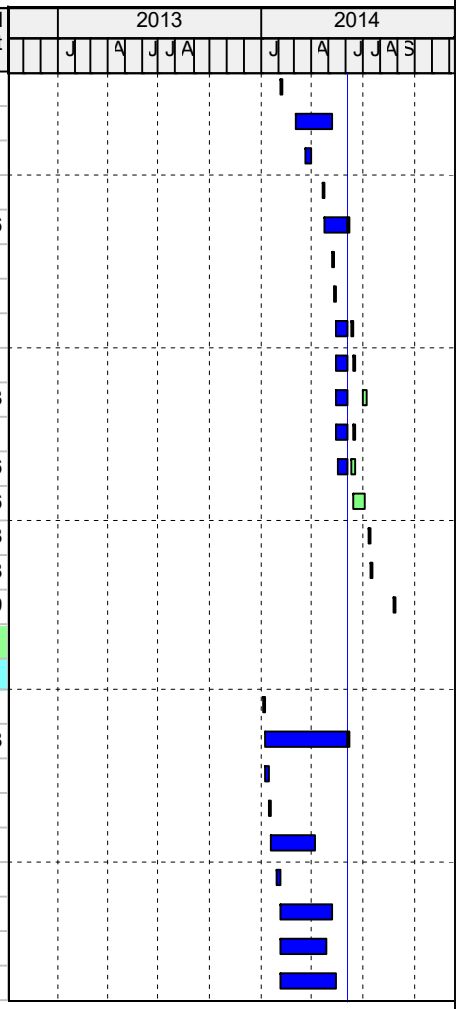



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 30-Apr-14 A | |
| LL1-6016 | Electrical RI | 20 | 2 | 17-Feb-14 A | 18-Jun-14 | 11 |
| LL1-6018 | HVAC RI | 20 | 2 | 17-Feb-14 A | 18-Jun-14 | 11 |
| LL1-6022 | Fire Alarm / Elec Specialties RI | 20 | 2 | 17-Feb-14 A | 18-Jun-14 | 11 |
| LL1-Z2-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z2-6014 | Plumbing RI | 20 | 5 | 17-Feb-14 A | 13-Jun-14 | 8 |
| LL1-Z2-6016 | Electrical RI | 20 | 5 | 17-Feb-14 A | 13-Jun-14 | 8 |
| LL1-Z2-6018 | HVAC RI | 20 | 5 | 17-Feb-14 A | 13-Jun-14 | 8 |
| LL1-Z2-6022 | Fire Alarm / Elec Specialties RI | 20 | 5 | 17-Feb-14 A | 13-Jun-14 | 8 |
| LL1-Z3-6012 | Fire Sprinkler RI (At All Areas North of Q-Line) | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z3-6014 | Plumbing RI (At All Areas North of Q-Line) | 20 | 5 | 17-Feb-14 A | 23-Jun-14 | 24 |
| LL1-Z3-6016 | Electrical RI (At All Areas North of Q-Line) | 20 | 5 | 17-Feb-14 A | 23-Jun-14 | 24 |
| LL1-Z3-6018 | HVAC RI (At All Areas North of Q-Line) | 20 | 5 | 17-Feb-14 A | 23-Jun-14 | 24 |
| LL1-Z3-6022 | Fire Alarm / Elec Specialties RI (At All Areas North of | 20 | 5 | 17-Feb-14 A | 23-Jun-14 | 24 |
| LL1-Z2-6020 | Hollow Metal Door Frames | 5 | 0 | 17-Mar-14 A | 04-Apr-14 A | |
| LL1-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| LL1-Z3-6020 | Hollow Metal Door Frames (At All Areas North of Q-Lir | 1 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| L1B-6004 | CMU Walls [including East Service Corridor] | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L1L-6002 | Layout [including back of house] | 3 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 29-Apr-14 A | |
| L1B-6008 | Int Wall Framing & Inspection [including East Service | 6 | 1 | 21-Apr-14 A | 05-Jun-14 | 3 |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 5 | 1 | 25-Apr-14 A | 06-Jun-14 | 10 |
| LL1C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L1K-6004 | CMU Walls [including public restroom] | 3 | 0 | 05-May-14 A | 08-May-14 A | |
| L1K-6002 | Layout [including public restroom] | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| L1K-6008 | Int Wall Framing & Inspection [including public restroc | 4 | 2 | 09-May-14 A | 06-Jun-14 | 7 |

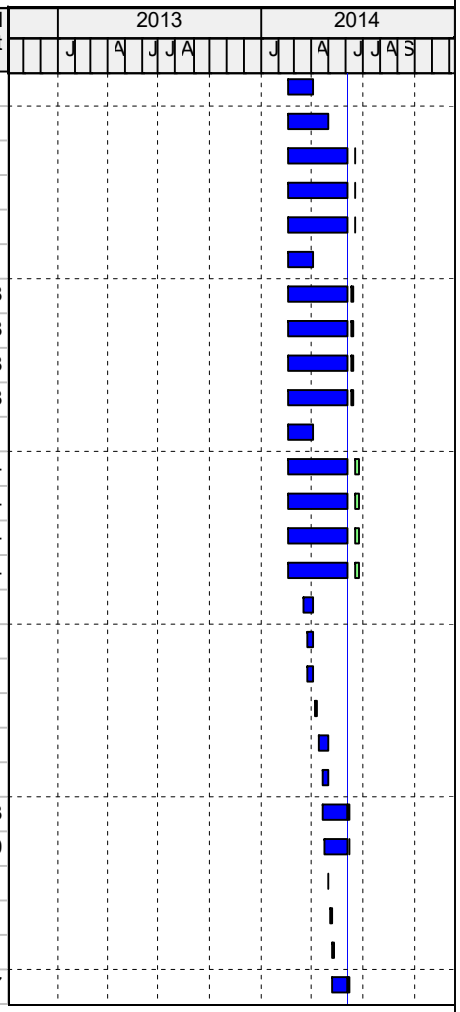


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-6002 | Layout [including East Service Corridor] | 3 | 0 | 14-May-14 A | 27-May-14 A | |
| L1L-6008 | Int Wall Framing & Inspection [including back of hous | 6 | 4 | 27-May-14 A | 10-Jun-14 | 0 |
| L1L-6004 | CMU Walls [including back of house] | 3 | 3 | 05-Jun-14 | 09-Jun-14 | 2 |
| LL1-6010 | CMU Seismic Clips | 2 | 2 | 09-Jun-14 | 10-Jun-14 | 15 |
| L1B-6010 | CMU Seismic Clips [including East Service Corridor] | 2 | 2 | 09-Jun-14 | 10-Jun-14 | 5 |
| L1K-6010 | CMU Seismic Clips [including public restroom] | 2 | 2 | 09-Jun-14 | 10-Jun-14 | 7 |
| LL1-Z2-6010 | CMU Seismic Clips | 2 | 2 | 11-Jun-14 | 12-Jun-14 | 9 |
| L1K-6012 | Fire Sprinkler RI [including public restroom] | 10 | 10 | 11-Jun-14 | 24-Jun-14 | 17 |
| L1K-6014 | Plumbing RI [including public restroom] | 10 | 10 | 11-Jun-14 | 24-Jun-14 | 7 |
| L1L-6010 | CMU Seismic Clips [including back of house] | 2 | 2 | 12-Jun-14 | 13-Jun-14 | 2 |
| LL1-Z3-6010 | CMU Seismic Clips (At All Areas North of Q-Line) | 2 | 2 | 13-Jun-14 | 16-Jun-14 | 24 |
| L1B-6012 | Fire Sprinkler RI [including East Service Corridor] | 10 | 10 | 13-Jun-14 | 26-Jun-14 | 8 |
| L1B-6014 | Plumbing RI [including East Service Corridor] | 10 | 10 | 13-Jun-14 | 26-Jun-14 | 3 |
| LL1-Z2-6009 | Frame Ceilings | 10 | 10 | 16-Jun-14 | 27-Jun-14 | 8 |
| L1L-6012 | Fire Sprinkler RI [including back of house] | 10 | 10 | 18-Jun-14 | 01-Jul-14 | 5 |
| L1L-6014 | Plumbing RI [including back of house] | 10 | 10 | 18-Jun-14 | 01-Jul-14 | 0 |
| L1K-6016 | Electrical RI [including public restroom] | 10 | 10 | 18-Jun-14 | 01-Jul-14 | 7 |
| L1K-6018 | HVAC RI [including public restroom] | 10 | 10 | 18-Jun-14 | 01-Jul-14 | 12 |
| LL1-6009 | Frame Ceilings | 10 | 10 | 19-Jun-14 | 02-Jul-14 | 11 |
| L1B-6016 | Electrical RI [including East Service Corridor] | 10 | 10 | 20-Jun-14 | 03-Jul-14 | 3 |
| L1B-6018 | HVAC RI [including East Service Corridor] | 10 | 10 | 20-Jun-14 | 03-Jul-14 | 3 |
| LL1-Z3-6009 | Frame Ceilings (At All Areas North of Q-Line) | 3 | 3 | 24-Jun-14 | 26-Jun-14 | 24 |
| L1L-6016 | Electrical RI [including back of house] | 10 | 10 | 25-Jun-14 | 09-Jul-14 | 0 |
| L1L-6018 | HVAC RI [including back of house] | 10 | 10 | 25-Jun-14 | 09-Jul-14 | 0 |
| L1K-6022 | Fire Alarm / Elec Specialties RI [including public restro | 10 | 10 | 25-Jun-14 | 09-Jul-14 | 7 |
| LL1-Z3C-6012 | Complete Fire Sprinkler RI @ Ceilings (At All Areas Nc | 5 | 5 | 27-Jun-14 | 03-Jul-14 | 34 |
| LL1-Z3C-6014 | Complete Plumbing RI @ Ceilings (At All Areas North | 5 | 5 | 27-Jun-14 | 03-Jul-14 | 24 |

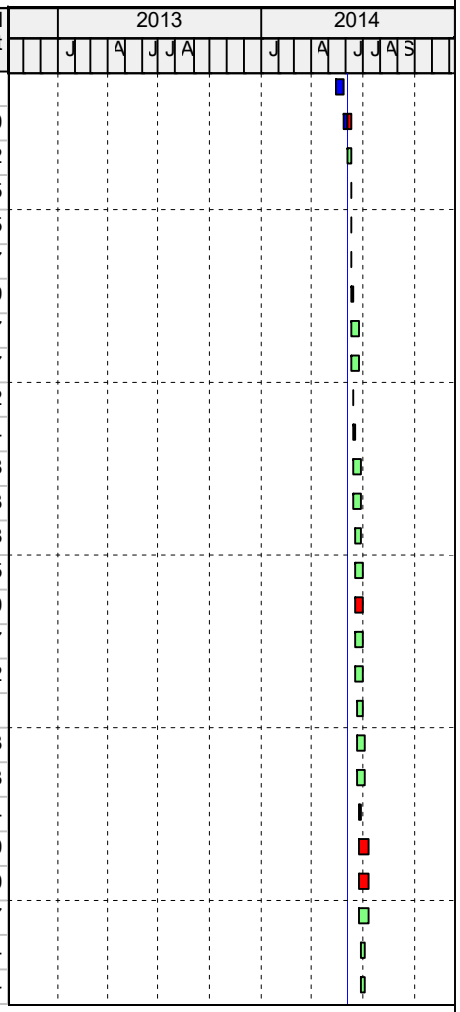


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-6022 | Fire Alarm / Elec Specialties RI [including East Service | 10 | 10 | 27-Jun-14 | 11-Jul-14 | 3 |
| LL1-Z2C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 5 | 30-Jun-14 | 07-Jul-14 | 18 |
| LL1-Z2C-6014 | Complete Plumbing RI @ Ceilings | 5 | 5 | 30-Jun-14 | 07-Jul-14 | 8 |
| L1L-6022 | Fire Alarm / Elec Specialties RI [including back of hou | 10 | 10 | 02-Jul-14 | 16-Jul-14 | 0 |
| LL1C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 18 |
| LL1C-6016 | Complete Electrical RI @ Ceilings | 7 | 7 | 03-Jul-14 | 14-Jul-14 | 11 |
| LL1C-6018 | Complete HVAC RI @ Ceilings | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 18 |
| LL1-Z3C-6016 | Complete Electrical RI @ Ceilings (At All Areas North | 5 | 5 | 07-Jul-14 | 11-Jul-14 | 24 |
| LL1-Z3C-6018 | Complete HVAC RI @ Ceilings (At All Areas North of | 5 | 5 | 07-Jul-14 | 11-Jul-14 | 29 |
| L1B-6009 | Frame Ceilings [including East Service Corridor] | 10 | 10 | 07-Jul-14 | 18-Jul-14 | 3 |
| LL1-Z2C-6016 | Complete Electrical RI @ Ceilings | 5 | 5 | 08-Jul-14 | 14-Jul-14 | 8 |
| LL1-Z2C-6018 | Complete HVAC RI @ Ceilings | 5 | 5 | 08-Jul-14 | 14-Jul-14 | 13 |
| L1L-6009 | Frame Ceilings [including back of house] | 10 | 10 | 10-Jul-14 | 23-Jul-14 | 0 |
| L1K-6009 | Frame Ceilings [including public restroom] | 10 | 10 | 10-Jul-14 | 23-Jul-14 | 7 |
| LL1-Z3C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 5 | 14-Jul-14 | 18-Jul-14 | 24 |
| LL1C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 11 |
| LL1-Z2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 8 |
| LL1-Z3-6024 | Inspections for Cover (At All Areas North of Q-Line) | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 24 |
| L1B-6020 | Hollow Metal Door Frames [including East Service Co | 5 | 5 | 21-Jul-14 | 25-Jul-14 | 15 |
| L1BC-6012 | Complete Fire Sprinkler RI @ Ceilings [including East | 5 | 5 | 21-Jul-14 | 25-Jul-14 | 15 |
| L1BC-6014 | Complete Plumbing RI @ Ceilings [including East Se | 5 | 5 | 21-Jul-14 | 25-Jul-14 | 3 |
| LL1-6024 | Inspections for Cover | 2 | 2 | 22-Jul-14 | 23-Jul-14 | 11 |
| LL1-Z2-6024 | Inspections for Cover | 2 | 2 | 22-Jul-14 | 23-Jul-14 | 8 |
| L1L-6020 | Hollow Metal Door Frames [including back of house] | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 10 |
| L1LC-6012 | Complete Fire Sprinkler RI @ Ceilings [including back | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 10 |
| L1LC-6014 | Complete Plumbing RI @ Ceilings [including back of | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 0 |
| L1K-6020 | Hollow Metal Door Frames [including public restroom] | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 17 |

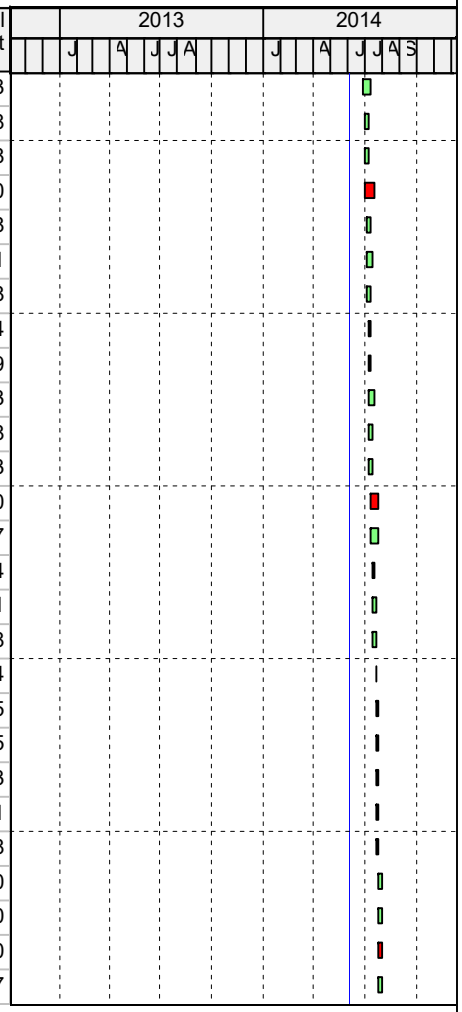


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1KC-6012 | Complete Fire Sprinkler RI @ Ceilings [including publi | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 17 |
| L1KC-6014 | Complete Plumbing RI @ Ceilings [including public re | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 7 |
| L1BC-6016 | Complete Electrical RI @ Ceilings [including East Ser | 7 | 7 | 28-Jul-14 | 05-Aug-14 | 3 |
| L1BC-6018 | Complete HVAC RI @ Ceilings [including East Service | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 10 |
| L1LC-6016 | Complete Electrical RI @ Ceilings [including back of h | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 0 |
| L1LC-6018 | Complete HVAC RI @ Ceilings [including back of hou | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 5 |
| L1KC-6016 | Complete Electrical RI @ Ceilings [including public res | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 7 |
| L1KC-6018 | Complete HVAC RI @ Ceilings [including public restro | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 12 |
| L1BC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings \| | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 3 |
| L1LC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings \| | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 0 |
| L1KC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings \| | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 7 |
| L1B-6024 | Inspections for Cover [including East Service Corridor] | 2 | 2 | 13-Aug-14 | 14-Aug-14 | 3 |
| L1L-6024 | Inspections for Cover [including back of house] | 2 | 2 | 14-Aug-14 | 15-Aug-14 | 0 |
| L1K-6024 | Inspections for Cover [including public restroom] | 2 | 2 | 14-Aug-14 | 15-Aug-14 | 7 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 0 | 17-Apr-14 A | 09-May-14 A | |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6006 | L2 - Support Frame/Sheathing for Metal Panels | 10 | 3 | 21-Mar-14 A | 08-Jul-14 | 6 |
| L02-6008 | L2 - Int Wall Framing | 10 | 2 | 25-Apr-14 A | 10-Jul-14 | 6 |
| L02-6014 | L2 - Plumbing RI | 15 | 15 | 28-Apr-14 A | 31-Jul-14 | 6 |
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 0 | 28-Apr-14 A | 09-May-14 A | |
| L02-6004 | L2 - CMU Walls | 5 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L02-6002 | L2 - Layout | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L02-6012 | L2 - Fire Sprinkler RI | 10 | 10 | 11-Jul-14 | 24-Jul-14 | 16 |
| L02-6016 | L2 - Electrical RI | 10 | 10 | 11-Jul-14 | 24-Jul-14 | 11 |
| L02-6018 | L2 - HVAC RI (including equipment) | 20 | 20 | 11-Jul-14 | 07-Aug-14 | 6 |

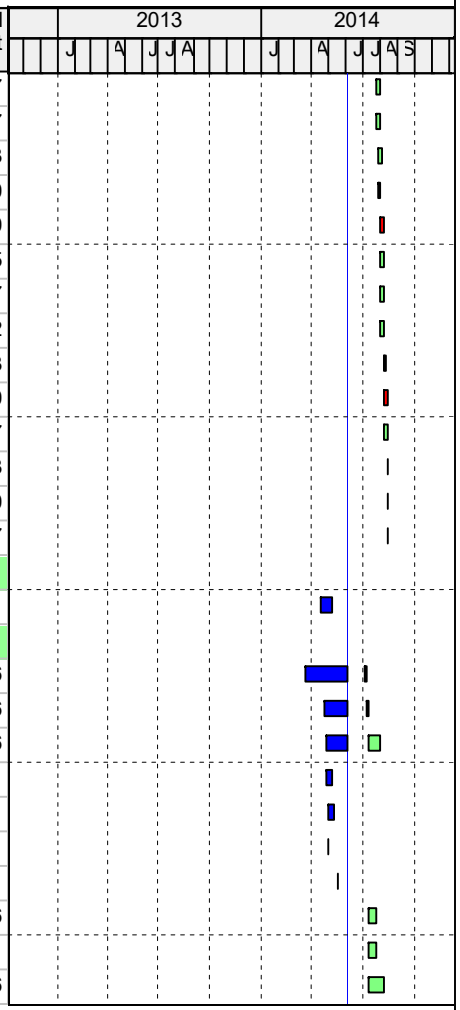



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-6020 | L2 - H Mtl Frames | 5 | 5 | 11-Jul-14 | 17-Jul-14 | 21 |
| L02-6022 | L2 - Fire Alarm / Elec Specialties Rl | 10 | 10 | 18-Jul-14 | 31-Jul-14 | 11 |
| L02-6024 | L2 - Inspections | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 6 |
| Upper Tower - (Levels 3 thru PH) | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L07-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 01-Apr-11 A | 11-Apr-11 A | |
| L04-6012 | Fire Sprinkler Mains | 5 | 0 | 01-Feb-14 A | 03-Apr-14 A | |
| L03-8219 | HVAC Risers | 5 | 0 | 11-Feb-14 A | 23-Mar-14 A | |
| L03-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 11-Feb-14 A | 03-Mar-14 A | |
| L03-6002 | Layout | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| L04-8219 | HVAC Risers | 5 | 0 | 13-Feb-14 A | 23-Mar-14 A | |
| L05-8219 | HVAC Risers | 5 | 0 | 17-Feb-14 A | 03-Mar-14 A | |
| L03-6008 | Frame Shaft Walls | 3 | 0 | 18-Feb-14 A | 26-Mar-14 A | |
| L04-6002 | Layout | 5 | 0 | 19-Feb-14 A | 25-Feb-14 A | |
| L04-6008 | Frame Shaft Walls | 3 | 0 | 20-Feb-14 A | 26-Mar-14 A | |
| L03-6011 | PreRock Shafts | 2 | 0 | 24-Feb-14 A | 25-Mar-14 A | |
| L03-6010 | Frame Walls | 5 | 0 | 25-Feb-14 A | 25-Mar-14 A | |
| L05-6002 | Layout | 5 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| L04-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 28-Feb-14 A | 05-Mar-14 A | |
| L03-6016 | Electrical Rl | 5 | 0 | 03-Mar-14 A | 04-Apr-14 A | |
| L03-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 12-Mar-14 A | |
| L04-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 13-Mar-14 A | |
| L04-6010 | Frame Walls | 5 | 1 | 04-Mar-14 A | 09-Jun-14 | 37 |
| L05-6008 | Frame Shaft Walls | 3 | 0 | 05-Mar-14 A | 27-Mar-14 A | |
| L06-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L07-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L05-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 06-Mar-14 A | 21-Mar-14 A | |

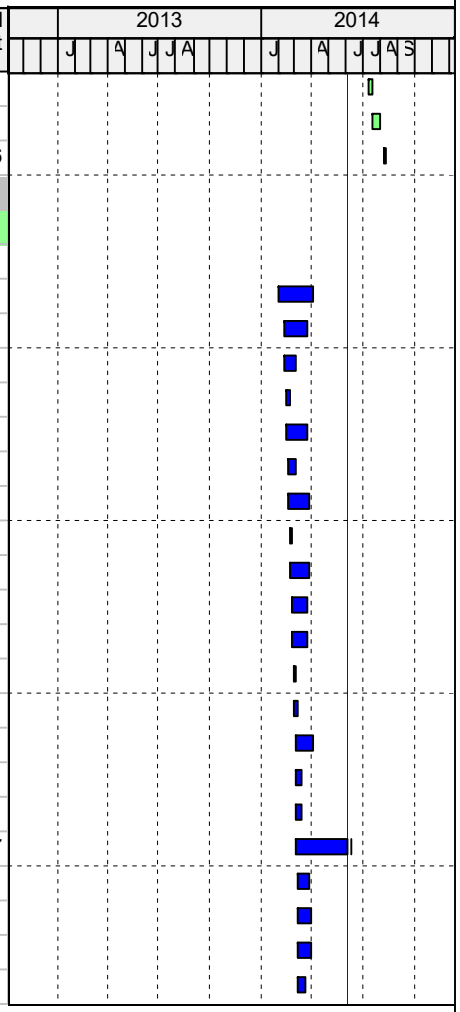



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6020 | Install Hollow Metal Frames | 3 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L04-6020 | Install Hollow Metal Frames | 3 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L05-6010 | Frame Walls | 5 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L06-6002 | Layout | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L04-6011 | PreRock Shafts | 2 | 0 | 18-Mar-14 A | 25-Mar-14 A | |
| L05-6009 | Inspect Shafts | 1 | 0 | 18-Mar-14 A | 18-Mar-14 A | |
| L05-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| L06-6008 | Frame Shaft Walls | 3 | 0 | 19-Mar-14 A | 03-Apr-14 A | |
| L06-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 27-Mar-14 A | |
| L04-6016 | Electrical RI | 5 | 0 | 20-Mar-14 A | 09-Apr-14 A | |
| L05-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 26-Mar-14 A | |
| L06-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 07-Apr-14 A | |
| L07-6002 | Layout | 5 | 0 | 24-Mar-14 A | 30-Apr-14 A | |
| L03-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L03-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L05-6016 | Electrical RI | 5 | 1 | 25-Mar-14 A | 05-Jun-14 | 48 |
| L04-6019 | Complete Top Out GWB | 2 | 2 | 26-Mar-14 A | 11-Jun-14 | 37 |
| L05-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L06-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| L03-6019 | Complete Top Out GWB | 2 | 0 | 27-Mar-14 A | 02-May-14 A | |
| L08-6002 | Layout | 5 | 0 | 27-Mar-14 A | 02-Apr-14 A | |
| L05-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 28-Mar-14 A | 03-Apr-14 A | |
| L06-6010 | Frame Walls | 5 | 0 | 28-Mar-14 A | 07-Apr-14 A | |
| L03-6012 | Fire Sprinkler Mains | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L07-6008 | Frame Shaft Walls | 3 | 0 | 31-Mar-14 A | 03-Apr-14 A | |

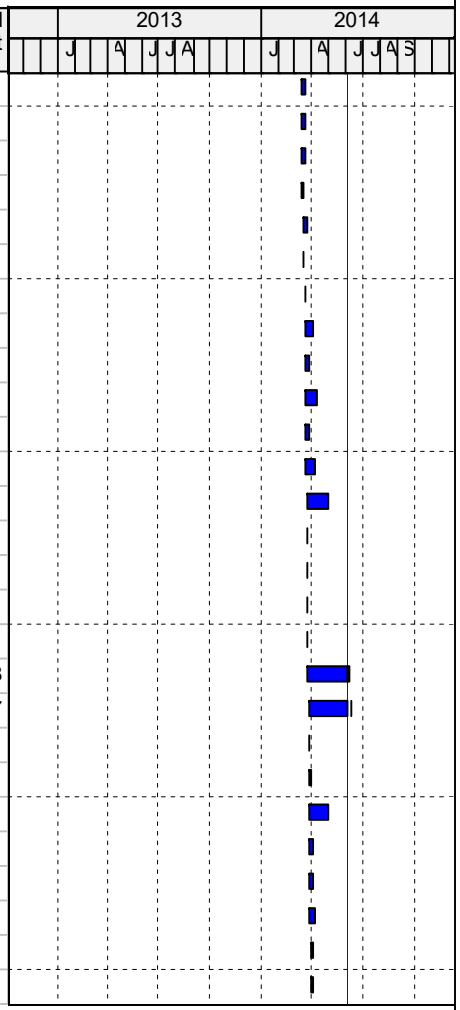



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6019 | Complete Top Out GWB | 2 | 0 | 01-Apr-14 A | 08-Apr-14 A | |
| L08-6008 | Frame Shaft Walls | 3 | 0 | 02-Apr-14 A | 21-Apr-14 A | |
| L03-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L04-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L05-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L06-6016 | Electrical RI | 5 | 0 | 03-Apr-14 A | 15-Apr-14 A | |
| L07-6009 | Inspect Shafts | 1 | 0 | 03-Apr-14 A | 03-Apr-14 A | |
| L07-6011 | PreRock Shafts | 2 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| L05-6012 | Fire Sprinkler Mains | 5 | 0 | 04-Apr-14 A | 30-Apr-14 A | |
| L06-6012 | Fire Sprinkler Mains | 5 | 0 | 07-Apr-14 A | 30-Apr-14 A | |
| L06-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L06-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L07-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| L07-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L03-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L03-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L04-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L06-6009 | Inspect Shafts | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L06-6019 | Complete Top Out GWB | 2 | 0 | 08-Apr-14 A | 18-Apr-14 A | |
| L07-6010 | Frame Walls | 5 | 0 | 08-Apr-14 A | 15-Apr-14 A | |
| L08-6011 | PreRock Shafts | 2 | 0 | 08-Apr-14 A | 23-Apr-14 A | |
| L09-6002 | Layout | 5 | 0 | 08-Apr-14 A | 26-Apr-14 A | |
| L03-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 09-Apr-14 A | 08-May-14 A | |
| L03-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L05-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 09-Apr-14 A | 14-Apr-14 A | |
| L08-6009 | Inspect Shafts | 1 | 0 | 09-Apr-14 A | 25-Apr-14 A | |
| L09-6008 | Frame Shaft Walls | 3 | 0 | 11-Apr-14 A | 15-Apr-14 A | |

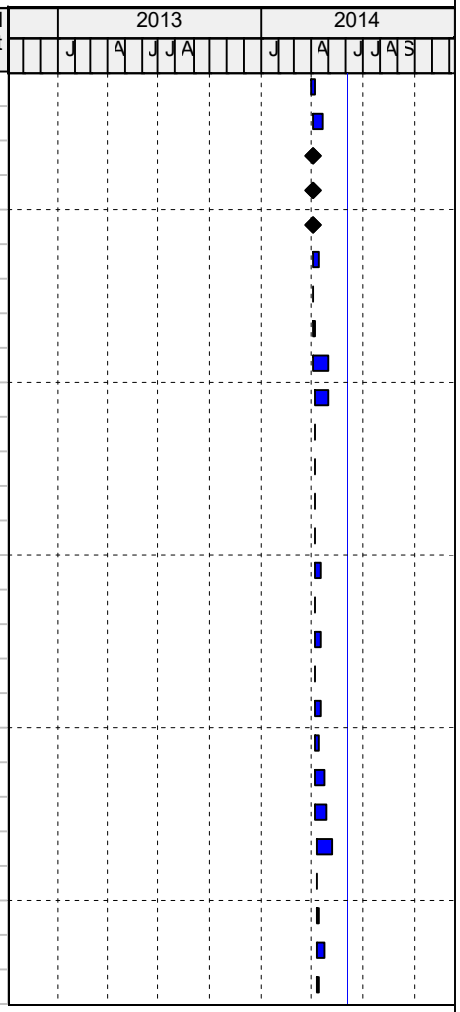



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| L04-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 15-Apr-14 A | 16-Apr-14 A | |
| L07-6012 | Fire Sprinkler Mains | 5 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| L07-6016 | Electrical RI | 5 | 0 | 15-Apr-14 A | 12-May-14 A | |
| L07-6020 | Install Hollow Metal Frames | 3 | 0 | 16-Apr-14 A | 23-Apr-14 A | |
| L05-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 17-Apr-14 A | 25-Apr-14 A | |
| L06-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 17-Apr-14 A | 12-May-14 A | |
| L06-6023 | Inspection of Exterior Framing | 0 | 0 | 17-Apr-14 A | | |
| L09-8219 | HVAC Risers | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L09-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L04-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 18-Apr-14 A | 20-Apr-14 A | |
| L04-6028 | PreRock at Heat Pumps | 2 | 0 | 20-Apr-14 A | 22-Apr-14 A | |
| L08-8219 | HVAC Risers | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6009 | Inspect Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6011 | PreRock Shafts | 2 | 0 | 22-Apr-14 A | 24-Apr-14 A | |
| L04-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L06-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 23-Apr-14 A | 25-Apr-14 A | |
| L08-6020 | Install Hollow Metal Frames | 3 | 0 | 23-Apr-14 A | 13-May-14 A | |
| L11-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L11-8220 | Plumbing Risers - Install | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L04-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L09-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L10-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L10-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 20-May-14 A | |
| L12-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |

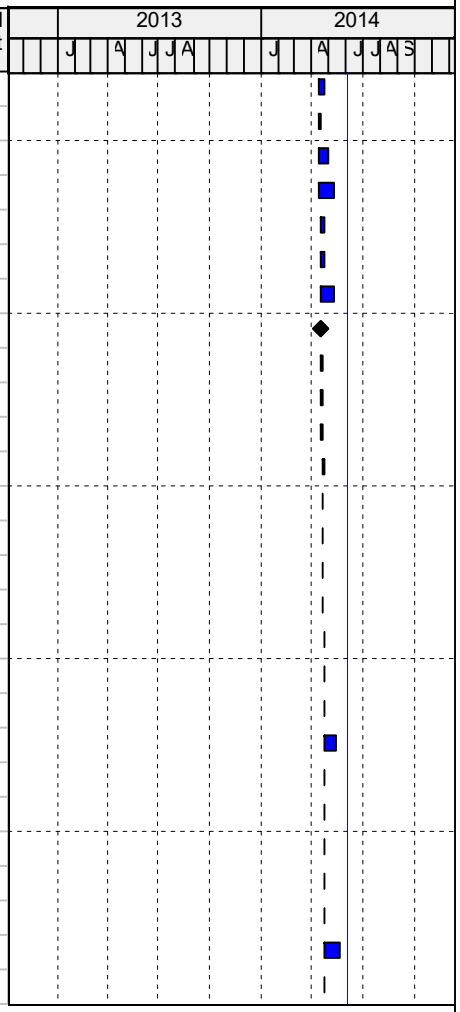



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 25-Apr-14 A | 13-Jun-14 | 37 |
| L04-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L09-6010 | Frame Walls | 5 | 0 | 25-Apr-14 A | 20-May-14 A | |
| L09-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L10-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L11-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 30-Apr-14 A | |
| L12-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L08-6010 | Frame Walls | 5 | 0 | 26-Apr-14 A | 30-Apr-14 A | |
| L10-6002 | Layout | 5 | 0 | 27-Apr-14 A | 27-Apr-14 A | |
| L04-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 28-Apr-14 A | 30-Apr-14 A | |
| L05-6018 | HVAC RI | 5 | 1 | 28-Apr-14 A | 05-Jun-14 | 48 |
| L05-6022 | Fire Alarm / Elec Specialties RI | 5 | 1 | 28-Apr-14 A | 05-Jun-14 | 48 |
| L05-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6028 | PreRock at Heat Pumps | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L07-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 28-Apr-14 A | 12-May-14 A | |
| L10-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-Apr-14 A | 22-May-14 A | |
| L11-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L12-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L05-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| L05-6028 | PreRock at Heat Pumps | 2 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L06-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 09-May-14 A | |
| L06-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L06-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |

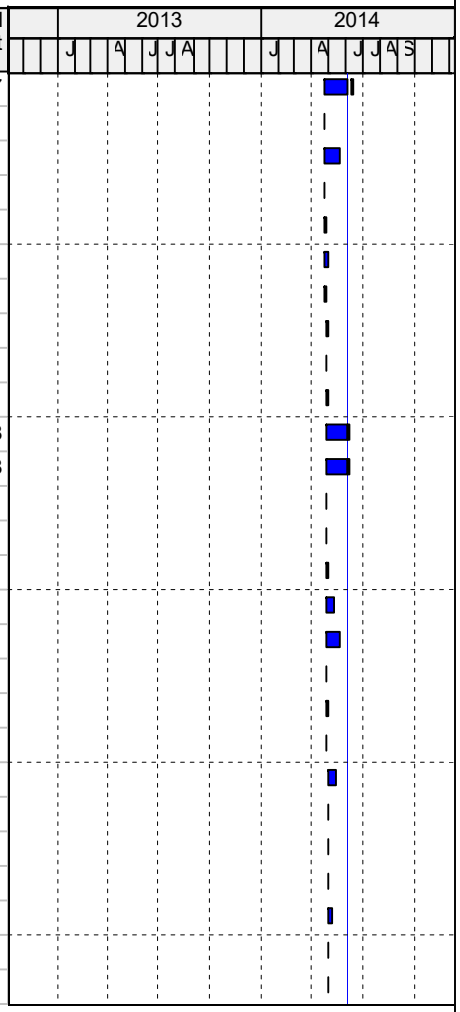



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L08-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L08-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L09-6020 | Install Hollow Metal Frames | 3 | 0 | 29-Apr-14 A | 20-May-14 A | |
| L09-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L10-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L04-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 30-Apr-14 A | 02-May-14 A | |
| L09-6019 | Complete Top Out GWB | 2 | 2 | 30-Apr-14 A | 06-Jun-14 | 59 |
| L11-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L12-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L03-6028 | PreRock at Heat Pumps | 2 | 0 | 01-May-14 A | 02-May-14 A | |
| L05-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L06-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L03-6014 | Set Tubs & Plumbing RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L05-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L05-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| L06-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L06-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 09-May-14 A | |
| L03-6018 | HVAC RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L03-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 06-May-14 A | 06-May-14 A | |
| L07-6014 | Set Tubs & Plumbing RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L07-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 06-May-14 A | 09-May-14 A | |
| L03-6004 | CMU Wall/Clips | 3 | 0 | 07-May-14 A | 08-May-14 A | |
| L03-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-May-14 A | 07-May-14 A | |

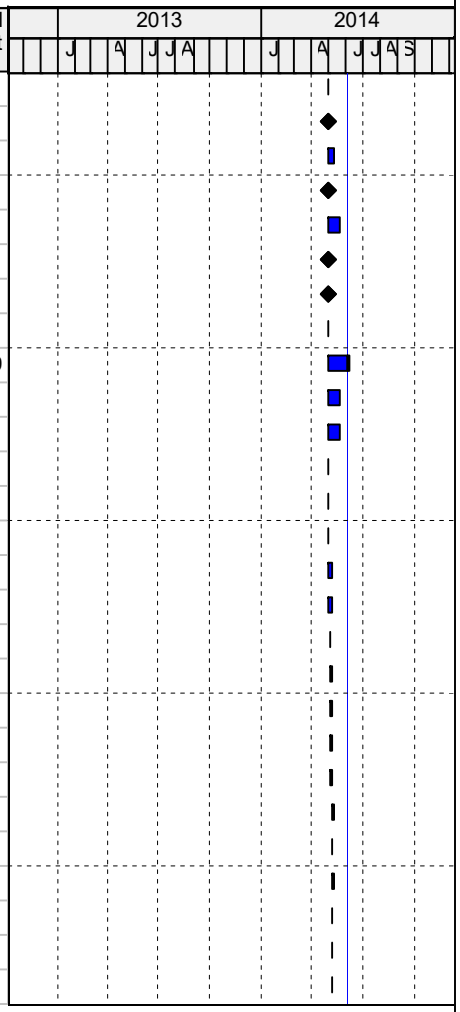


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 08-May-14 A | 13-May-14 A | |
| L03-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6004 | CMU Walls | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6018 | HVAC Rl | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L11-6010 | Frame Walls | 5 | 0 | 09-May-14 A | 15-May-14 A | |
| L05-6014 | Set Tubs & Plumbing Rl | 5 | 1 | 12-May-14 A | 05-Jun-14 | 48 |
| L07-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 12-May-14 A | 13-May-14 A | |
| L11-6020 | Install Hollow Metal Frames | 3 | 0 | 12-May-14 A | 14-May-14 A | |
| L11-6019 | Complete Top Out GWB | 2 | 0 | 12-May-14 A | 14-May-14 A | |
| L14-6002 | Layout | 5 | 0 | 12-May-14 A | 14-May-14 A | |
| L15-6002 | Layout | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L05-6004 | CMU Walls | 3 | 0 | 13-May-14 A | 13-May-14 A | |
| L06-6018 | HVAC Rl | 5 | 1 | 13-May-14 A | 05-Jun-14 | 50 |
| L06-6022 | Fire Alarm / Elec Specialties Rl | 5 | 1 | 13-May-14 A | 05-Jun-14 | 50 |
| L07-6018 | HVAC Rl | 5 | 1 | 13-May-14 A | 05-Jun-14 | 55 |
| L07-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| L07-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 13-May-14 A | 13-May-14 A | |
| L14-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L16-6002 | Layout | 5 | 0 | 13-May-14 A | 16-May-14 A | |
| L06-6004 | CMU Walls | 3 | 0 | 14-May-14 A | 14-May-14 A | |
| L07-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 15-May-14 A | |
| L08-6012 | Fire Sprinkler Mains | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6002 | Layout | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L07-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |

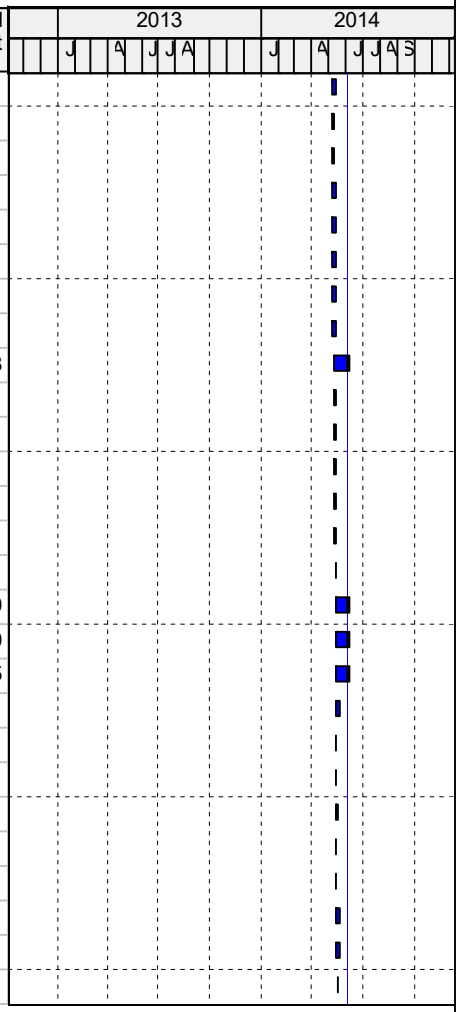



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6014 | Set Tubs & Plumbing RI | 5 | 5 | 16-May-14 A | 11-Jun-14 | 51 |
| L08-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L11-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L12-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L07-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L08-6028 | PreRock at Heat Pumps | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L09-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L10-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L11-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L15-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 19-May-14 A | 19-May-14 A | |
| L07-6028 | PreRock at Heat Pumps | 2 | 0 | 20-May-14 A | 21-May-14 A | |
| L07-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L08-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 20-May-14 A | 21-May-14 A | |
| L10-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L11-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L14-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L07-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 21-May-14 A | 27-May-14 A | |
| L08-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L08-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L09-6028 | PreRock at Heat Pumps | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L10-6014 | Set Tubs & Plumbing RI | 5 | 2 | 21-May-14 A | 06-Jun-14 | 54 |
| L10-6010 | Frame Walls | 5 | 0 | 21-May-14 A | 03-Jun-14 A | |

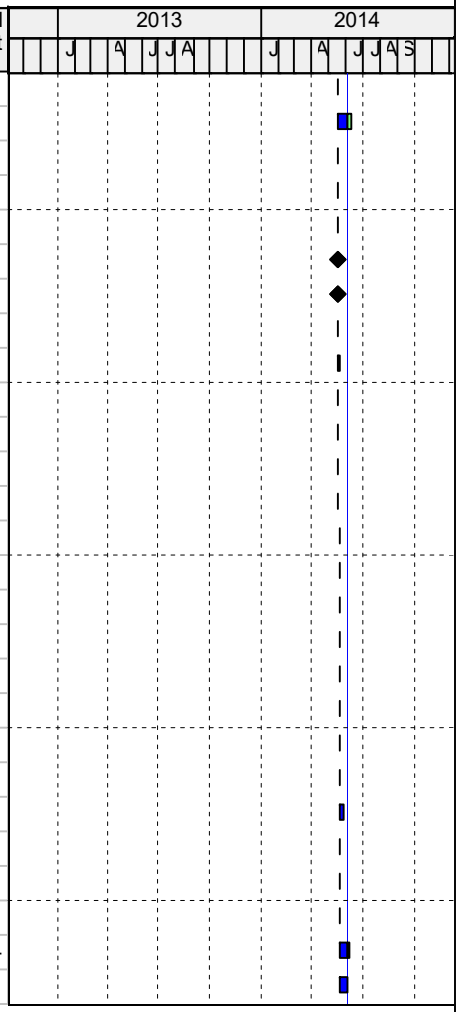



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-6019 | Complete Top Out GWB | 2 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L11-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L12-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L14-8220 | Plumbing Risers - Install | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L15-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L16-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L07-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| L08-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 22-May-14 A | 22-May-14 A | |
| L10-6012 | Fire Sprinkler Mains | 5 | 0 | 22-May-14 A | 27-May-14 A | |
| L08-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L09-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6020 | Install Hollow Metal Frames | 3 | 0 | 23-May-14 A | 03-Jun-14 A | |
| L10-6028 | PreRock at Heat Pumps | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L14-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L15-8220 | Plumbing Risers - Install | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L09-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 27-May-14 A | 27-May-14 A | |
| L12-6010 | Frame Walls | 5 | 0 | 27-May-14 A | 02-Jun-14 A | |
| L08-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L09-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 28-May-14 A | 28-May-14 A | |
| L10-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 28-May-14 A | 03-Jun-14 A | |
| L14-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L15-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-May-14 A | 30-May-14 A | |
| L16-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 28-May-14 A | 28-May-14 A | |
| L16-8220 | Plumbing Risers - Install | 2 | 0 | 28-May-14 A | 29-May-14 A | |
| L08-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 29-May-14 A | 30-May-14 A | |
| L10-6016 | Electrical RI | 5 | 2 | 29-May-14 A | 10-Jun-14 | 54 |

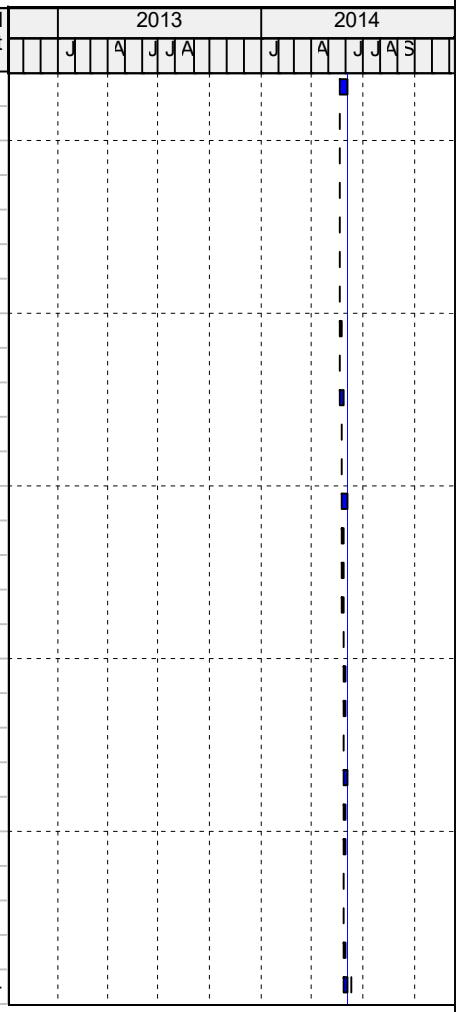



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-6018 | HVAC RI | 5 | 2 | 29-May-14 A | 10-Jun-14 | 59 |
| L10-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L10-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| L12-6012 | Fire Sprinkler Mains | 5 | 2 | 30-May-14 A | 06-Jun-14 | 48 |
| L12-6020 | Install Hollow Metal Frames | 3 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L15-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L17-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L17-8220 | Plumbing Risers - Install | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L10-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L11-6016 | Electrical RI | 5 | 5 | 02-Jun-14 A | 16-Jun-14 | 46 |
| L12-6019 | Complete Top Out GWB | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L14-6020 | Install Hollow Metal Frames | 3 | 1 | 02-Jun-14 A | 05-Jun-14 | 65 |
| L14-6010 | Frame Walls | 5 | 0 | 02-Jun-14 A | 04-Jun-14 A | |
| L16-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| L14-6019 | Complete Top Out GWB | 2 | 1 | 03-Jun-14 A | 05-Jun-14 | 53 |
| L16-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 2 | 03-Jun-14 A | 06-Jun-14 | 19 |
| L10-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| L17-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 1 | 04-Jun-14 A | 05-Jun-14 | 11 |
| L08-6016 | Electrical RI | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 51 |
| L08-6018 | HVAC RI | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 51 |
| L08-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 51 |
| L08-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 05-Jun-14 | 09-Jun-14 | 53 |
| L09-6012 | Fire Sprinkler Mains | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 56 |
| L09-6014 | Set Tubs & Plumbing RI | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 48 |
| L09-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 4 | 05-Jun-14 | 10-Jun-14 | 10 |
| L10-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 05-Jun-14 | 09-Jun-14 | 60 |
| L11-6028 | PreRock at Heat Pumps | 2 | 2 | 05-Jun-14 | 06-Jun-14 | 13 |

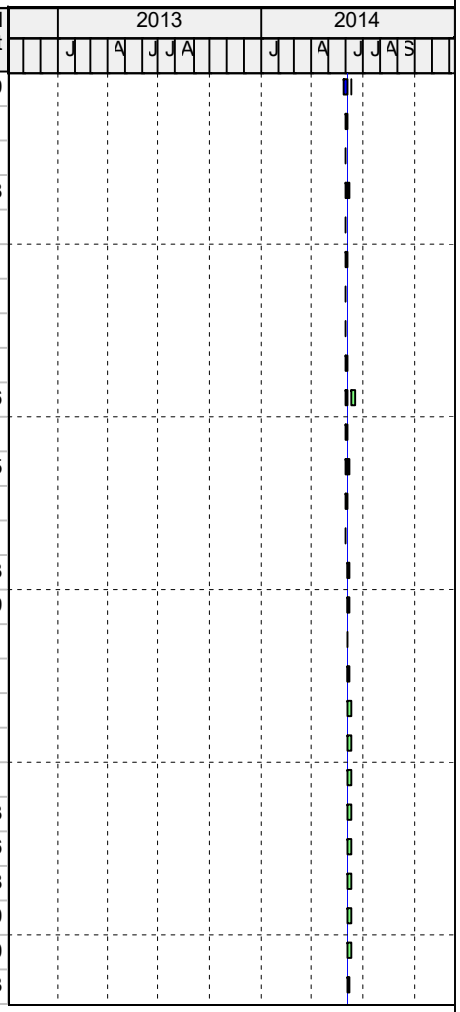


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 4 | 05-Jun-14 | 10-Jun-14 | 123 |
| L14-6012 | Fire Sprinkler Mains | 5 | 5 | 05-Jun-14 | 11-Jun-14 | 46 |
| L14-6023 | Inspection of Exterior Framing | 0 | 0 | 05-Jun-14 | | 17 |
| L15-6010 | Frame Walls | 3 | 3 | 05-Jun-14 | 09-Jun-14 | 14 |
| L15-6023 | Inspection of Exterior Framing | 0 | 0 | 05-Jun-14 | | 14 |
| L16-6023 | Inspection of Exterior Framing | 0 | 0 | 05-Jun-14 | | 23 |
| L09-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 06-Jun-14 | 10-Jun-14 | 59 |
| L09-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 06-Jun-14 | 09-Jun-14 | 56 |
| L12-6014 | Set Tubs & Plumbing Rl | 4 | 4 | 06-Jun-14 | 11-Jun-14 | 48 |
| L12-6028 | PreRock at Heat Pumps | 2 | 2 | 06-Jun-14 | 09-Jun-14 | 16 |
| L16-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 06-Jun-14 | 06-Jun-14 | 23 |
| L17-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 4 | 06-Jun-14 | 11-Jun-14 | 11 |
| L17-6023 | Inspection of Exterior Framing | 0 | 0 | 06-Jun-14 | | 24 |
| L11-6012 | Fire Sprinkler Mains | 4 | 4 | 09-Jun-14 | 12-Jun-14 | 50 |
| L11-6014 | Set Tubs & Plumbing Rl | 4 | 4 | 09-Jun-14 | 12-Jun-14 | 47 |
| L11-6029 | Inspection of PreRock at Heat Pumps | 1 | 1 | 09-Jun-14 | 09-Jun-14 | 13 |
| L14-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 09-Jun-14 | 09-Jun-14 | 16 |
| L15-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 09-Jun-14 | 09-Jun-14 | 19 |
| L16-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 1 | 09-Jun-14 | 09-Jun-14 | 23 |
| L11-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 4 | 10-Jun-14 | 13-Jun-14 | 46 |
| L11-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 10-Jun-14 | 12-Jun-14 | 46 |
| L11-6030 | Tape/Firecaulk at Heat Pumps | 1 | 1 | 10-Jun-14 | 10-Jun-14 | 13 |
| L12-6029 | Inspection of PreRock at Heat Pumps | 1 | 1 | 10-Jun-14 | 10-Jun-14 | 16 |
| L14-6014 | Set Tubs & Plumbing Rl | 4 | 4 | 10-Jun-14 | 13-Jun-14 | 46 |
| L14-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 4 | 10-Jun-14 | 13-Jun-14 | 120 |
| L14-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 1 | 10-Jun-14 | 10-Jun-14 | 16 |
| L15-6020 | Install Hollow Metal Frames | 3 | 3 | 10-Jun-14 | 12-Jun-14 | 34 |

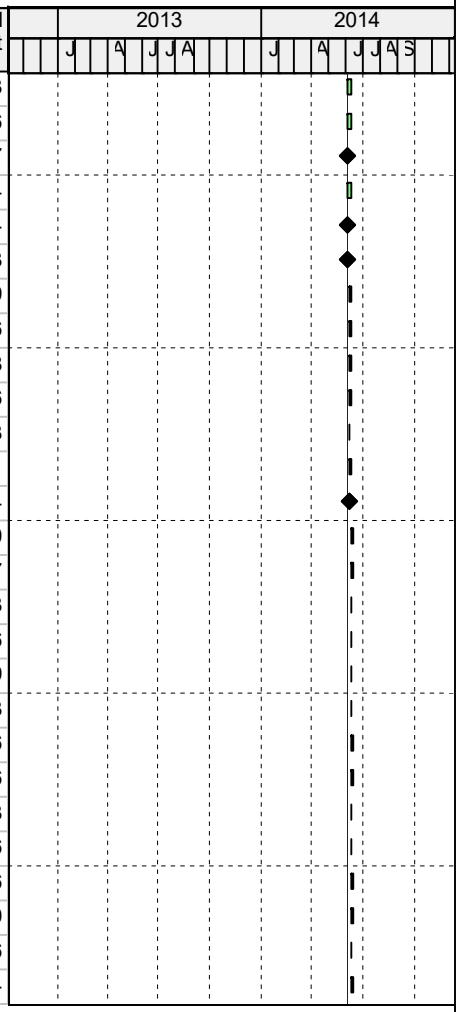



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6019 | Complete Top Out GWB | 2 | 2 | 10-Jun-14 | 11-Jun-14 | 14 |
| L15-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 1 | 10-Jun-14 | 10-Jun-14 | 19 |
| L10-6022 | Fire Alarm / Elec Specialties Rl | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 54 |
| L10-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 4 | 11-Jun-14 | 16-Jun-14 | 10 |
| L11-6018 | HVAC Rl | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 47 |
| L11-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 11-Jun-14 | 13-Jun-14 | 50 |
| L11-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 1 | 11-Jun-14 | 11-Jun-14 | 13 |
| L12-6030 | Tape/Firecaulk at Heat Pumps | 1 | 1 | 11-Jun-14 | 11-Jun-14 | 16 |
| L14-6028 | PreRock at Heat Pumps | 2 | 2 | 11-Jun-14 | 12-Jun-14 | 16 |
| L17-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 11-Jun-14 | 11-Jun-14 | 23 |
| L03-6024 | Inspections for GWB Cover | 1 | 1 | 12-Jun-14 | 12-Jun-14 | 37 |
| L09-6016 | Electrical Rl | 5 | 5 | 12-Jun-14 | 18-Jun-14 | 48 |
| L09-6018 | HVAC Rl | 5 | 5 | 12-Jun-14 | 18-Jun-14 | 53 |
| L09-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 12-Jun-14 | 16-Jun-14 | 56 |
| L10-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 12-Jun-14 | 13-Jun-14 | 52 |
| L12-6221 | Frame Ceilings & Furring Walls | 4 | 4 | 12-Jun-14 | 17-Jun-14 | 48 |
| L12-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 1 | 12-Jun-14 | 12-Jun-14 | 16 |
| L15-6012 | Fire Sprinkler Mains | 3 | 3 | 12-Jun-14 | 16-Jun-14 | 16 |
| L15-6014 | Set Tubs & Plumbing Rl | 5 | 5 | 12-Jun-14 | 18-Jun-14 | 14 |
| L15-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 4 | 12-Jun-14 | 17-Jun-14 | 118 |
| L17-6004 | CMU Walls | 3 | 3 | 12-Jun-14 | 16-Jun-14 | 15 |
| L17-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 1 | 12-Jun-14 | 12-Jun-14 | 23 |
| L11-6022 | Fire Alarm / Elec Specialties Rl | 4 | 4 | 13-Jun-14 | 18-Jun-14 | 46 |
| L14-6029 | Inspection of PreRock at Heat Pumps | 1 | 1 | 13-Jun-14 | 13-Jun-14 | 16 |
| L15-6028 | PreRock at Heat Pumps | 2 | 2 | 13-Jun-14 | 16-Jun-14 | 17 |
| L14-6221 | Frame Ceilings & Furring Walls | 2 | 2 | 16-Jun-14 | 17-Jun-14 | 46 |
| L14-6030 | Tape/Firecaulk at Heat Pumps | 1 | 1 | 16-Jun-14 | 16-Jun-14 | 16 |

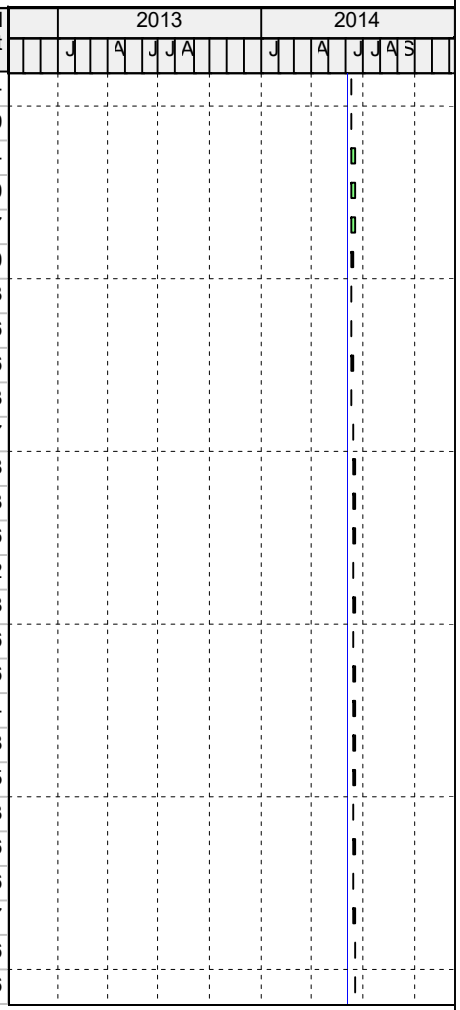



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 4 | 16-Jun-14 | 19-Jun-14 | 19 |
| L04-6024 | Inspections for GWB Cover | 1 | 1 | 17-Jun-14 | 17-Jun-14 | 36 |
| L05-6024 | Inspections for GWB Cover | 1 | 1 | 17-Jun-14 | 17-Jun-14 | 41 |
| L06-6024 | Inspections for GWB Cover | 1 | 1 | 17-Jun-14 | 17-Jun-14 | 43 |
| L07-6024 | Inspections for GWB Cover | 1 | 1 | 17-Jun-14 | 17-Jun-14 | 48 |
| L11-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 4 | 17-Jun-14 | 20-Jun-14 | 10 |
| L12-6016 | Electrical RI | 4 | 4 | 17-Jun-14 | 20-Jun-14 | 48 |
| L12-6018 | HVAC RI | 4 | 4 | 17-Jun-14 | 20-Jun-14 | 51 |
| L12-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 17-Jun-14 | 19-Jun-14 | 53 |
| L14-6016 | Electrical RI | 4 | 4 | 17-Jun-14 | 20-Jun-14 | 46 |
| L14-6018 | HVAC RI | 4 | 4 | 17-Jun-14 | 20-Jun-14 | 51 |
| L14-6013 | Fire Sprinkler Branch Lines | 2 | 2 | 17-Jun-14 | 18-Jun-14 | 54 |
| L14-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 1 | 17-Jun-14 | 17-Jun-14 | 16 |
| L15-6029 | Inspection of PreRock at Heat Pumps | 1 | 1 | 17-Jun-14 | 17-Jun-14 | 17 |
| L16-6028 | PreRock at Heat Pumps | 2 | 2 | 17-Jun-14 | 18-Jun-14 | 18 |
| L11-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 18-Jun-14 | 19-Jun-14 | 41 |
| L15-6030 | Tape/Firecaulk at Heat Pumps | 1 | 1 | 18-Jun-14 | 18-Jun-14 | 17 |
| L09-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 19-Jun-14 | 25-Jun-14 | 48 |
| L15-6221 | Frame Ceilings & Furring Walls | 4 | 4 | 19-Jun-14 | 24-Jun-14 | 14 |
| L15-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 1 | 19-Jun-14 | 19-Jun-14 | 17 |
| L16-6029 | Inspection of PreRock at Heat Pumps | 1 | 1 | 19-Jun-14 | 19-Jun-14 | 18 |
| L17-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 4 | 19-Jun-14 | 24-Jun-14 | 11 |
| L17-6028 | PreRock at Heat Pumps | 2 | 2 | 19-Jun-14 | 20-Jun-14 | 19 |
| L08-6024 | Inspections for GWB Cover | 1 | 1 | 20-Jun-14 | 20-Jun-14 | 45 |
| L10-6024 | Inspections for GWB Cover | 1 | 1 | 20-Jun-14 | 20-Jun-14 | 52 |
| L12-6022 | Fire Alarm / Elec Specialties RI | 4 | 4 | 20-Jun-14 | 25-Jun-14 | 48 |
| L16-6010 | Frame Walls | 5 | 5 | 20-Jun-14 | 26-Jun-14 | 19 |

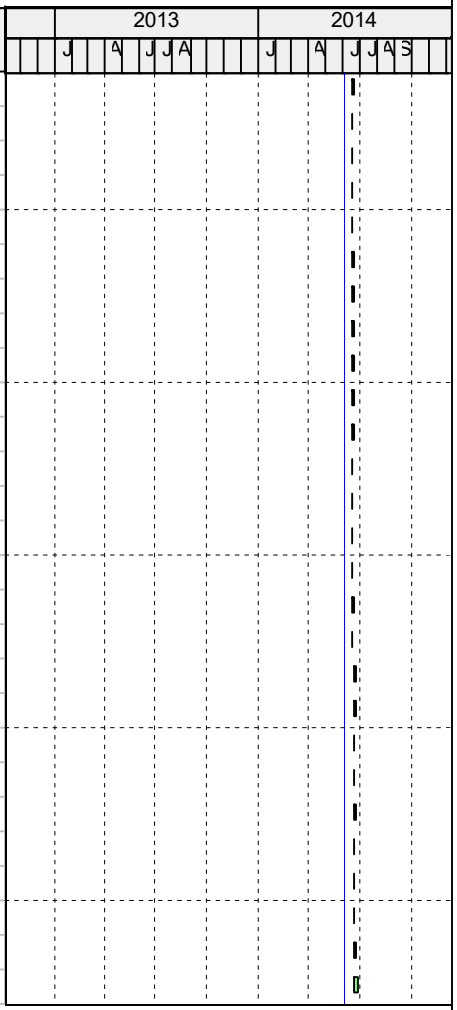



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6030 | Tape/Firecaulk at Heat Pumps | 1 | 1 | 20-Jun-14 | 20-Jun-14 | 18 |
| L12-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 3 | 23-Jun-14 | 25-Jun-14 | 10 |
| L14-6022 | Fire Alarm / Elec Specialties Rl | 5 | 5 | 23-Jun-14 | 27-Jun-14 | 46 |
| L16-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 1 | 23-Jun-14 | 23-Jun-14 | 18 |
| L17-6029 | Inspection of PreRock at Heat Pumps | 1 | 1 | 23-Jun-14 | 23-Jun-14 | 19 |
| L12-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 24-Jun-14 | 25-Jun-14 | 45 |
| L17-6030 | Tape/Firecaulk at Heat Pumps | 1 | 1 | 24-Jun-14 | 24-Jun-14 | 19 |
| L03-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 25-Jun-14 | 03-Jul-14 | 44 |
| L15-6016 | Electrical Rl | 4 | 4 | 25-Jun-14 | 30-Jun-14 | 14 |
| L15-6018 | HVAC Rl | 4 | 4 | 25-Jun-14 | 30-Jun-14 | 19 |
| L15-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 25-Jun-14 | 27-Jun-14 | 21 |
| L17-6010 | Frame Walls | 5 | 5 | 25-Jun-14 | 01-Jul-14 | 11 |
| L17-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 1 | 25-Jun-14 | 25-Jun-14 | 19 |
| L09-6024 | Inspections for GWB Cover | 1 | 1 | 26-Jun-14 | 26-Jun-14 | 48 |
| L11-6024 | Inspections for GWB Cover | 1 | 1 | 26-Jun-14 | 26-Jun-14 | 41 |
| L14-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 3 | 26-Jun-14 | 30-Jun-14 | 10 |
| L16-6012 | Fire Sprinkler Mains | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 27 |
| L16-6014 | Set Tubs & Plumbing Rl | 5 | 5 | 26-Jun-14 | 02-Jul-14 | 19 |
| L14-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 27-Jun-14 | 30-Jun-14 | 41 |
| L16-6020 | Install Hollow Metal Frames | 3 | 3 | 27-Jun-14 | 01-Jul-14 | 33 |
| L16-6019 | Complete Top Out GWB | 2 | 2 | 27-Jun-14 | 30-Jun-14 | 29 |
| L04-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 30-Jun-14 | 09-Jul-14 | 41 |
| L16-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 30-Jun-14 | 02-Jul-14 | 29 |
| L12-6024 | Inspections for GWB Cover | 1 | 1 | 01-Jul-14 | 01-Jul-14 | 45 |
| L15-6022 | Fire Alarm / Elec Specialties Rl | 5 | 5 | 01-Jul-14 | 08-Jul-14 | 14 |
| L15-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 3 | 01-Jul-14 | 03-Jul-14 | 10 |
| L17-6012 | Fire Sprinkler Mains | 5 | 5 | 01-Jul-14 | 08-Jul-14 | 19 |

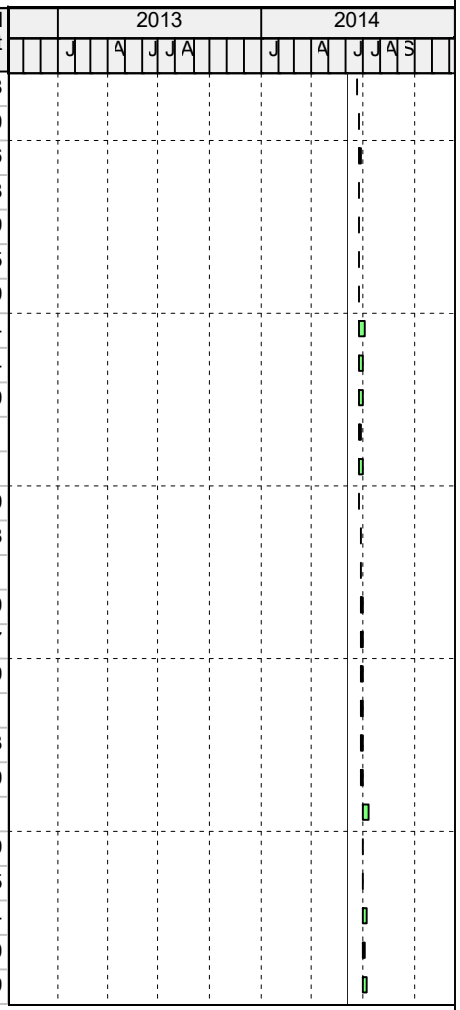



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6014 | Set Tubs & Plumbing RI | 5 | 5 | 01-Jul-14 | 08-Jul-14 | 11 |
| L15-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 02-Jul-14 | 03-Jul-14 | 12 |
| L17-6020 | Install Hollow Metal Frames | 3 | 3 | 02-Jul-14 | 07-Jul-14 | 25 |
| L17-6019 | Complete Top Out GWB | 2 | 2 | 02-Jul-14 | 03-Jul-14 | 21 |
| L16-6016 | Electrical RI | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 19 |
| L16-6018 | HVAC RI | 5 | 5 | 03-Jul-14 | 10-Jul-14 | 24 |
| L16-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 03-Jul-14 | 08-Jul-14 | 27 |
| L17-6221 | Frame Ceilings & Furring Walls | 3 | 3 | 03-Jul-14 | 08-Jul-14 | 21 |
| L05-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 07-Jul-14 | 15-Jul-14 | 37 |
| L16-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 3 | 07-Jul-14 | 09-Jul-14 | 10 |
| L14-6024 | Inspections for GWB Cover | 1 | 1 | 08-Jul-14 | 08-Jul-14 | 41 |
| L16-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 08-Jul-14 | 09-Jul-14 | 21 |
| L17-6016 | Electrical RI | 5 | 5 | 09-Jul-14 | 15-Jul-14 | 11 |
| L17-6018 | HVAC RI | 5 | 5 | 09-Jul-14 | 15-Jul-14 | 16 |
| L17-6013 | Fire Sprinkler Branch Lines | 3 | 3 | 09-Jul-14 | 11-Jul-14 | 19 |
| L06-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 10-Jul-14 | 18-Jul-14 | 48 |
| L17-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 3 | 10-Jul-14 | 14-Jul-14 | 10 |
| L15-6024 | Inspections for GWB Cover | 1 | 1 | 11-Jul-14 | 11-Jul-14 | 12 |
| L16-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 11-Jul-14 | 17-Jul-14 | 19 |
| L17-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 11-Jul-14 | 14-Jul-14 | 13 |
| L17-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 16-Jul-14 | 22-Jul-14 | 11 |
| L07-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 17-Jul-14 | 25-Jul-14 | 43 |
| L08-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 17-Jul-14 | 25-Jul-14 | 43 |
| L11-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 18-Jul-14 | 28-Jul-14 | 42 |
| L12-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 18-Jul-14 | 28-Jul-14 | 42 |
| L16-6024 | Inspections for GWB Cover | 1 | 1 | 18-Jul-14 | 18-Jul-14 | 19 |
| L17-6024 | Inspections for GWB Cover | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 11 |

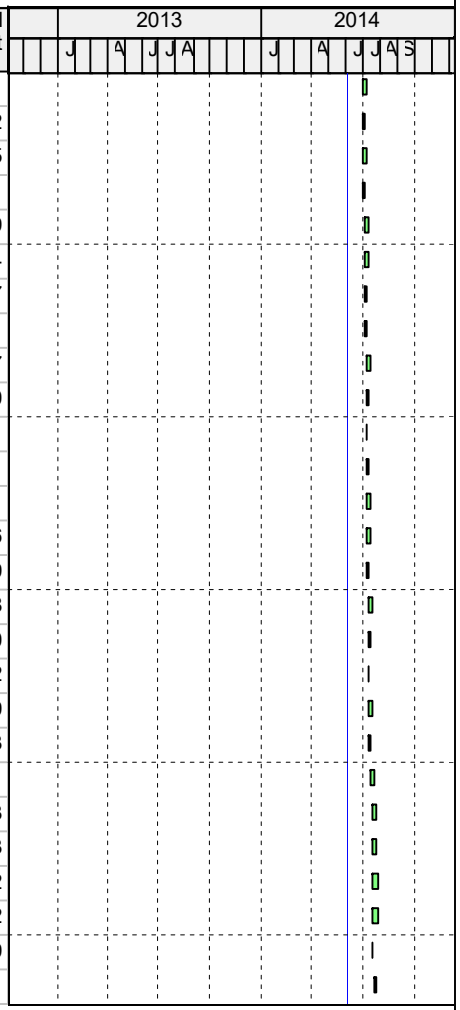



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 28-Jul-14 | 05-Aug-14 | 36 |
| L10-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 28-Jul-14 | 05-Aug-14 | 36 |
| L15-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 28-Jul-14 | 05-Aug-14 | 22 |
| L14-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 29-Jul-14 | 06-Aug-14 | 35 |
| L16-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 31-Jul-14 | 08-Aug-14 | 19 |
| L17-6000 | Skim Ceiling/Tape GWB | 7 | 7 | 06-Aug-14 | 14-Aug-14 | 10 |
| **Mechanical Penthouse** | | | | | | |
| PH-6006 | PH - Exterior Wall Framing (including PH roof parapet | 6 | 6 | 05-Jun-14 | 12-Jun-14 | 9 |
| PH-6002 | PH - Layout | 1 | 1 | 13-Jun-14 | 13-Jun-14 | 10 |
| PH-6008 | PH - Interior Wall Framing | 3 | 3 | 16-Jun-14 | 18-Jun-14 | 10 |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 5 | 16-Jun-14 | 20-Jun-14 | 20 |
| PH-6014 | PH - Plumbing/Piping RI | 40 | 40 | 16-Jun-14 | 11-Aug-14 | 10 |
| PH-6012 | PH - Fire Sprinkler RI | 10 | 10 | 19-Jun-14 | 02-Jul-14 | 37 |
| PH-6018 | PH - HVAC RI | 30 | 30 | 19-Jun-14 | 31-Jul-14 | 17 |
| PH-6020 | PH - H Mtl Frames | 2 | 2 | 19-Jun-14 | 20-Jun-14 | 50 |
| PH-6022 | PH - Fire Alarm / Elec Specialties RI | 5 | 5 | 19-Jun-14 | 25-Jun-14 | 42 |
| PH-6016 | PH - Electrical RI | 25 | 25 | 23-Jun-14 | 28-Jul-14 | 20 |
| PH-6024 | PH - Inspections | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 10 |
| **Finishes** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL4-8100 | LL4 - Insulation | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 27 |
| LL4-8102 | LL4 - GWB Hang / Tape / Finish | 8 | 8 | 16-Jul-14 | 25-Jul-14 | 27 |
| LL4-8104 | LL4 - Int Painting | 3 | 3 | 24-Jul-14 | 28-Jul-14 | 47 |
| LL4-8108 | LL4 - Elec Trim / Finish | 6 | 6 | 29-Jul-14 | 05-Aug-14 | 47 |
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 5 | 5 | 29-Jul-14 | 04-Aug-14 | 52 |

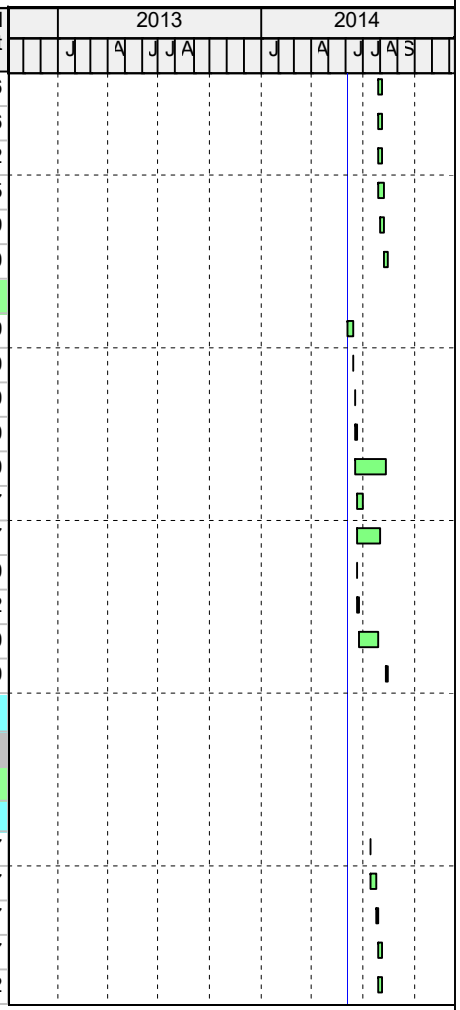



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8122 | LL4 - Plumbing Trim / Finish | 2 | 2 | 05-Aug-14 | 06-Aug-14 | 54 |
| LL4-8110 | LL4 - HVAC Trim / Finish | 2 | 2 | 06-Aug-14 | 07-Aug-14 | 49 |
| LL4-8118 | LL4 - Elec Specialties Trim / Finish | 4 | 4 | 06-Aug-14 | 11-Aug-14 | 47 |
| LL4-8124 | LL4 - Flooring | 3 | 3 | 12-Aug-14 | 14-Aug-14 | 47 |
| LL4-8126 | LL4 - Doors & Hardware | 3 | 3 | 13-Aug-14 | 15-Aug-14 | 47 |
| LL4-8114 | LL4 - Striping / Signage | 3 | 3 | 15-Aug-14 | 19-Aug-14 | 50 |
| LL4-8130 | LL4 - Substantially Complete | 0 | 0 | | 15-Aug-14 | 47 |
| LL4-8132 | LL4 - Contractor Pre-Punchlist | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 50 |
| LL4-8134 | LL4 - Pre-Clean | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 47 |
| LL4-8208 | LL4 - Final Clean | 3 | 3 | 25-Aug-14 | 27-Aug-14 | 47 |
| LL4-8210 | LL4 - Owner Walk / Create Punchlist | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 47 |
| LL4-8212 | LL4 - Final Punchlist | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 47 |
| LL4-8214 | LL4 - Floor Complete | 0 | 0 | | 05-Sep-14 | 47 |
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL3-8100 | LL3 - Insulation | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 27 |
| LL3-8102 | LL3 - GWB Hang / Tape / Finish | 8 | 8 | 21-Jul-14 | 30-Jul-14 | 27 |
| LL3-8104 | LL3 - Int Painting | 3 | 3 | 28-Jul-14 | 30-Jul-14 | 50 |
| LL3-8108 | LL3 - Elec Trim / Finish | 6 | 6 | 31-Jul-14 | 07-Aug-14 | 50 |
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 55 |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 2 | 2 | 07-Aug-14 | 08-Aug-14 | 57 |
| LL3-8110 | LL3 - HVAC Trim / Finish | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 52 |
| LL3-8118 | LL3 - Elec Specialties Trim / Finish | 4 | 4 | 08-Aug-14 | 13-Aug-14 | 50 |
| LL3-8124 | LL3 - Flooring | 3 | 3 | 14-Aug-14 | 18-Aug-14 | 50 |
| LL3-8126 | LL3 - Doors & Hardware | 3 | 3 | 15-Aug-14 | 19-Aug-14 | 50 |
| LL3-8114 | LL3 - Striping / Signage | 3 | 3 | 19-Aug-14 | 21-Aug-14 | 53 |
| LL3-8130 | LL3 - Substantially Complete | 0 | 0 | | 19-Aug-14 | 50 |

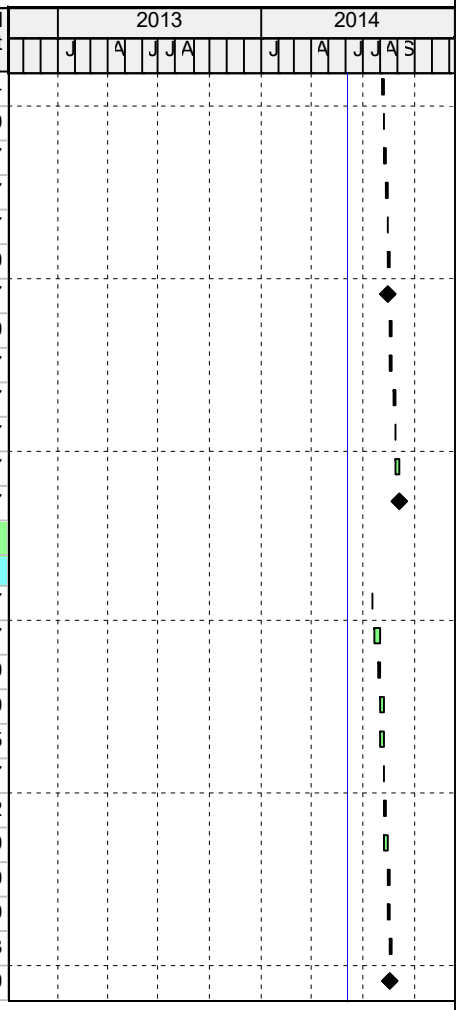



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-8132 | LL3 - Contractor Pre-Punchlist | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 53 |
| LL3-8134 | LL3 - Pre-Clean | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 50 |
| LL3-8208 | LL3 - Final Clean | 3 | 3 | 27-Aug-14 | 29-Aug-14 | 50 |
| LL3-8210 | LL3 - Owner Walk / Create Punchlist | 1 | 1 | 02-Sep-14 | 02-Sep-14 | 50 |
| LL3-8212 | LL3 - Final Punchlist | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 47 |
| LL3-8214 | LL3 - Floor Complete | 0 | 0 | | 12-Sep-14 | 47 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL2E-8102 | LL2 - GWB Hang / Tape / Finish @ Electrical Rooms | 8 | 8 | 09-Jul-14 | 18-Jul-14 | 38 |
| LL2-8100 | LL2 - Insulation | 3 | 3 | 21-Jul-14 | 23-Jul-14 | 27 |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish | 11 | 11 | 24-Jul-14 | 07-Aug-14 | 27 |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 10 | 10 | 24-Jul-14 | 06-Aug-14 | 59 |
| LL2-8104 | LL2 - Int Painting | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 27 |
| LL2-8120 | LL2 - Steel Pipe Guardrails | 6 | 6 | 08-Aug-14 | 15-Aug-14 | 57 |
| LL2-8108 | LL2 - Elec Trim / Finish | 10 | 10 | 12-Aug-14 | 25-Aug-14 | 27 |
| LL2-8112 | LL2 - Fire Sprinkler Trim / Finish | 8 | 8 | 12-Aug-14 | 21-Aug-14 | 41 |
| LL2-8116 | LL2 - Finish Carpentry / Millwork | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 47 |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 9 | 9 | 12-Aug-14 | 22-Aug-14 | 47 |
| LL2-8122 | LL2 - Plumbing Trim / Finish | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 48 |
| LL2-8128 | LL2 - Entry Gates | 3 | 3 | 25-Aug-14 | 27-Aug-14 | 47 |
| LL2-8110 | LL2 - HVAC Trim / Finish | 12 | 12 | 26-Aug-14 | 11-Sep-14 | 27 |
| LL2-8118 | LL2 - Elec Specialties Trim / Finish | 4 | 4 | 26-Aug-14 | 29-Aug-14 | 35 |
| LL2-8136 | LL2 - Chainlink Fencing / Gate @ Recycling | 2 | 2 | 28-Aug-14 | 29-Aug-14 | 47 |
| LL2-8124 | LL2 - Flooring | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 27 |
| LL2-8114 | LL2 - Striping / Signage | 3 | 3 | 19-Sep-14 | 23-Sep-14 | 36 |
| LL2-8126 | LL2 - Doors & Hardware | 7 | 7 | 19-Sep-14 | 29-Sep-14 | 27 |
| LL2-8130 | LL2 - Substantially Complete | 0 | 0 | | 29-Sep-14 | 27 |

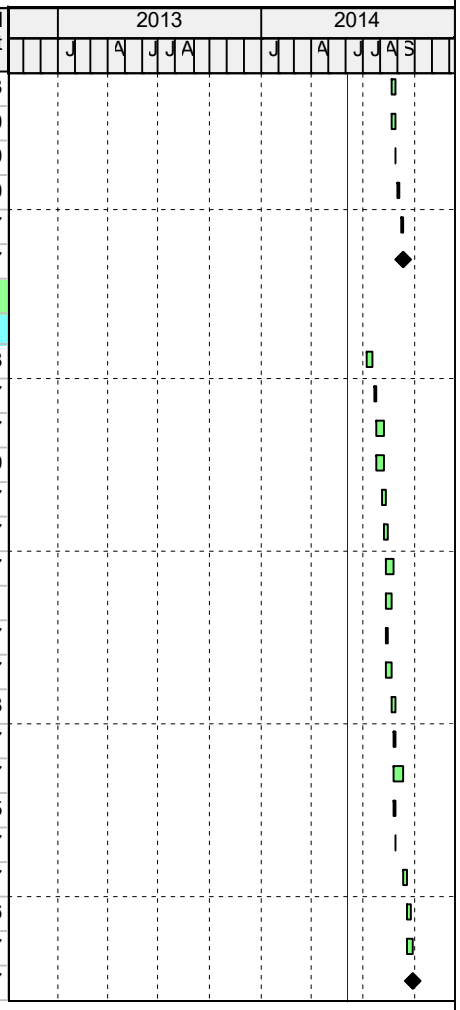



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-8132 | LL2 - Contractor Pre-Punchlist | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 30 |
| LL2-8134 | LL2 - Pre-Clean | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 27 |
| LL2-8208 | LL2 - Final Clean | 3 | 3 | 07-Oct-14 | 09-Oct-14 | 27 |
| LL2-8210 | LL2 - Owner Walk / Create Punchlist | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 27 |
| LL2-8212 | LL2 - Final Punchlist | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 27 |
| LL2-8214 | LL2 - Floor Complete | 0 | 0 | | 17-Oct-14 | 27 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1U-8102 | Above Ceiling GWB | 5 | 2 | 10-Feb-14 A | 16-Jun-14 | 11 |
| LL1-Z2U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 09-May-14 A | |
| LL1-Z3U-8102 | Above Ceiling GWB (At All Areas North of Q-Line) | 5 | 2 | 10-Feb-14 A | 16-Jun-14 | 24 |
| L1BU-8102 | Above Ceiling GWB [including East Service Corridor] | 5 | 5 | 06-Jun-14 | 12-Jun-14 | 3 |
| L1KU-8102 | Above Ceiling GWB [including public restroom] | 2 | 2 | 09-Jun-14 | 10-Jun-14 | 7 |
| L1LU-8102 | Above Ceiling GWB [including back of house] | 5 | 5 | 11-Jun-14 | 17-Jun-14 | 0 |
| LL1-Z3-8100 | Insulation | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 24 |
| LL1-Z3-8102 | GWB Hang | 5 | 5 | 23-Jul-14 | 29-Jul-14 | 24 |
| LL1-8100 | Insulation | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 11 |
| LL1-Z2-8100 | Insulation | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 8 |
| LL1-Z3-8215 | GWB Tape | 7 | 7 | 30-Jul-14 | 07-Aug-14 | 24 |
| LL1-8102 | GWB Hang | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 11 |
| LL1-Z2-8102 | GWB Hang | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 8 |
| LL1-8215 | GWB Tape | 7 | 7 | 07-Aug-14 | 15-Aug-14 | 11 |
| LL1-Z2-8215 | GWB Tape | 7 | 7 | 07-Aug-14 | 15-Aug-14 | 8 |
| LL1-Z3-8104 | Prime Paint | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 24 |
| LL1-Z3-8114 | T Bar Grid Ceiling | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 24 |
| LL1-Z3-8116 | Finish Carpentry / Millwork | 3 | 3 | 14-Aug-14 | 18-Aug-14 | 24 |
| L1B-8100 | Insulation | 4 | 4 | 15-Aug-14 | 20-Aug-14 | 3 |

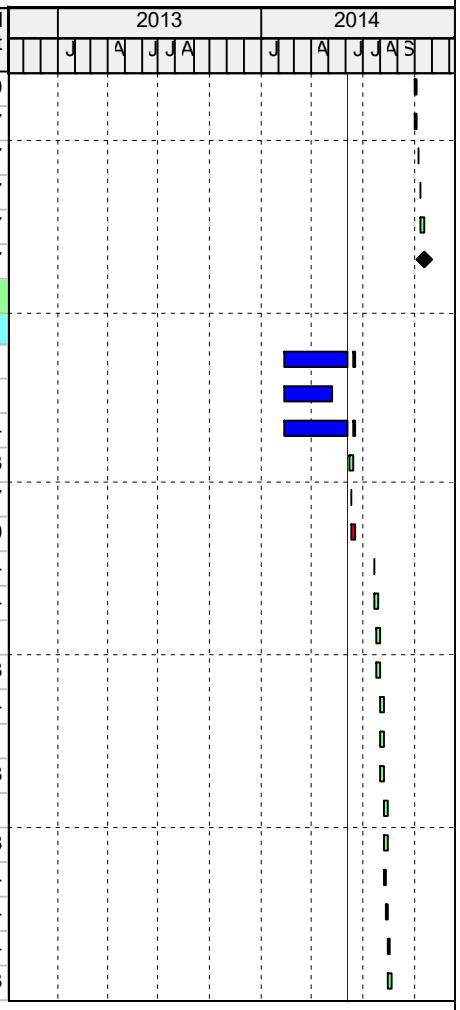



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-8104 | Prime Paint | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 11 |
| LL1-Z2-8104 | Prime Paint | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 8 |
| L1L-8100 | Insulation | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 0 |
| L1K-8100 | Insulation | 3 | 3 | 18-Aug-14 | 20-Aug-14 | 7 |
| LL1-Z3-8124 | Flooring | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 24 |
| L1B-8102 | GWB Hang | 6 | 6 | 21-Aug-14 | 28-Aug-14 | 3 |
| L1K-8102 | GWB Hang | 4 | 4 | 21-Aug-14 | 26-Aug-14 | 7 |
| LL1-8116 | Finish Carpentry / Millwork | 10 | 10 | 25-Aug-14 | 08-Sep-14 | 11 |
| LL1-8114 | T Bar Grid Ceiling | 3 | 3 | 25-Aug-14 | 27-Aug-14 | 23 |
| LL1-Z2-8114 | T Bar Grid Ceiling | 6 | 6 | 25-Aug-14 | 02-Sep-14 | 22 |
| LL1-Z3-8126 | Doors & Hardware | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 43 |
| LL1-Z3-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 3 | 3 | 25-Aug-14 | 27-Aug-14 | 48 |
| L1L-8102 | GWB Hang | 7 | 7 | 25-Aug-14 | 03-Sep-14 | 0 |
| LL1-Z3-8106 | Wallcoverings | 2 | 2 | 26-Aug-14 | 27-Aug-14 | 43 |
| L1K-8215 | GWB Tape | 6 | 6 | 27-Aug-14 | 04-Sep-14 | 7 |
| LL1-Z3-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 48 |
| LL1-Z3-8118 | Elec & Specialties Trim / Finish | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 46 |
| L1B-8215 | GWB Tape | 7 | 7 | 29-Aug-14 | 09-Sep-14 | 3 |
| LL1-Z2-8116 | Finish Carpentry / Millwork | 10 | 10 | 02-Sep-14 | 15-Sep-14 | 8 |
| L1L-8215 | GWB Tape | 9 | 9 | 04-Sep-14 | 16-Sep-14 | 0 |
| L1K-8104 | Prime Paint | 3 | 3 | 05-Sep-14 | 09-Sep-14 | 7 |
| LL1-Z3-8134 | Pre-Clean | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 46 |
| LL1-Z3-8132 | Contractor Pre-Punchlist | 3 | 3 | 10-Sep-14 | 12-Sep-14 | 46 |
| L1B-8104 | Prime Paint | 3 | 3 | 10-Sep-14 | 12-Sep-14 | 3 |
| L1K-8116 | Finish Carpentry / Millwork | 7 | 7 | 10-Sep-14 | 18-Sep-14 | 7 |
| L1K-8114 | T Bar Grid Ceiling | 3 | 3 | 10-Sep-14 | 12-Sep-14 | 14 |
| L1B-8116 | Finish Carpentry / Millwork | 10 | 10 | 15-Sep-14 | 26-Sep-14 | 3 |

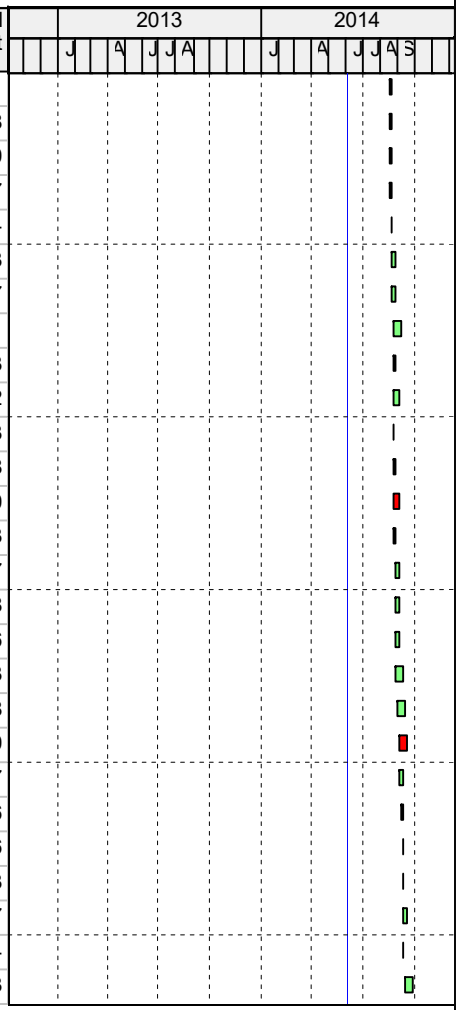



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-8124 | Flooring | 5 | 5 | 16-Sep-14 | 22-Sep-14 | 11 |
| L1L-8104 | Prime Paint | 3 | 3 | 17-Sep-14 | 19-Sep-14 | 0 |
| L1L-8116 | Finish Carpentry / Millwork | 10 | 10 | 22-Sep-14 | 03-Oct-14 | 0 |
| L1L-8114 | Install wood ceiling supports | 3 | 3 | 22-Sep-14 | 24-Sep-14 | 0 |
| LL1-8126 | Doors & Hardware | 3 | 3 | 23-Sep-14 | 25-Sep-14 | 11 |
| LL1-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 29 |
| LL1-Z2-8124 | Flooring | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 8 |
| L1B-8114 | T Bar Grid Ceiling | 3 | 3 | 24-Sep-14 | 26-Sep-14 | 3 |
| L1K-8124 | Flooring | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 7 |
| L1L-8124 | Flooring | 15 | 15 | 25-Sep-14 | 15-Oct-14 | 0 |
| LL1-8106 | Wallcoverings | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 11 |
| LL1-Z2-8126 | Doors & Hardware | 3 | 3 | 30-Sep-14 | 02-Oct-14 | 8 |
| LL1-Z2-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 21 |
| L1K-8126 | Doors & Hardware | 3 | 3 | 01-Oct-14 | 03-Oct-14 | 7 |
| L1K-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 3 | 3 | 01-Oct-14 | 03-Oct-14 | 22 |
| LL1-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 23 |
| LL1-8118 | Elec & Specialties Trim / Finish | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 11 |
| LL1-Z2-8106 | Wallcoverings | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 8 |
| L1B-8124 | Flooring | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 3 |
| L1K-8106 | Wallcoverings | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 7 |
| LL1-Z2-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 18 |
| LL1-Z2-8118 | Elec & Specialties Trim / Finish | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 8 |
| L1B-8126 | Doors & Hardware | 2 | 2 | 13-Oct-14 | 14-Oct-14 | 3 |
| L1B-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 2 | 2 | 13-Oct-14 | 14-Oct-14 | 11 |
| L1K-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 17 |
| L1K-8118 | Elec & Specialties Trim / Finish | 10 | 10 | 13-Oct-14 | 24-Oct-14 | 7 |
| L1B-8106 | Wallcoverings | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 3 |

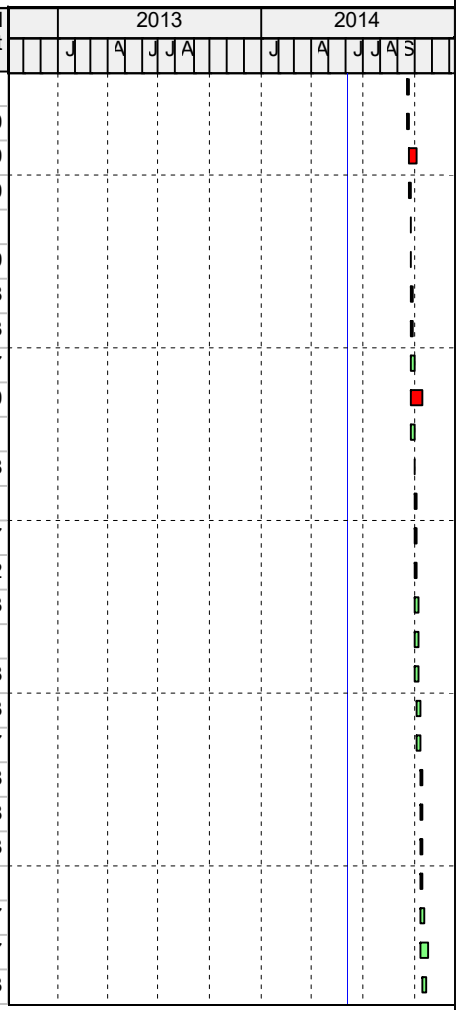



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-8134 | Pre-Clean | 3 | 3 | 17-Oct-14 | 21-Oct-14 | 11 |
| L1L-8126 | Doors & Hardware | 3 | 3 | 17-Oct-14 | 21-Oct-14 | 0 |
| L1L-8140 | Install wood ceiling | 8 | 8 | 17-Oct-14 | 28-Oct-14 | 5 |
| LL1-8132 | Contractor Pre-Punchlist | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 11 |
| LL1-Z2-8134 | Pre-Clean | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 8 |
| L1B-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 6 |
| L1B-8118 | Elec & Specialties Trim / Finish | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 3 |
| L1L-8106 | Wallcoverings | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 0 |
| LL1-Z2-8132 | Contractor Pre-Punchlist | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 8 |
| L1L-8118 | Elec & Specialties Trim / Finish | 7 | 7 | 27-Oct-14 | 04-Nov-14 | 0 |
| L1L-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 5 |
| L1K-8134 | Pre-Clean | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 7 |
| L1B-8134 | Pre-Clean | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 3 |
| L1K-8132 | Contractor Pre-Punchlist | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 7 |
| L1B-8132 | Contractor Pre-Punchlist | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 3 |
| L1L-8134 | Pre-Clean | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 0 |
| L1L-8132 | Contractor Pre-Punchlist | 3 | 3 | 11-Nov-14 | 13-Nov-14 | 0 |
| **Corridors / Common / Public Areas** | | | | | | |
| LL1-Z3-8200 | First Coat Finish Paint | 2 | 2 | 19-Aug-14 | 20-Aug-14 | 24 |
| LL1-Z3-8201 | Final Coat Finish Paint | 2 | 2 | 26-Aug-14 | 27-Aug-14 | 43 |
| LL1-Z3-8204 | Mech Trim / Finish (HVAC & Plumbing) | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 43 |
| LL1-8200 | First Coat Finish Paint | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 11 |
| LL1-Z3-8210 | Owner Walk / Create Punchlist | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 46 |
| LL1-Z2-8200 | First Coat Finish Paint | 5 | 5 | 16-Sep-14 | 22-Sep-14 | 8 |
| LL1-Z3-8212 | Final Punchlist | 3 | 3 | 16-Sep-14 | 18-Sep-14 | 46 |
| LL1-Z3-8208 | Final Clean | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 46 |
| L1K-8200 | First Coat Finish Paint | 3 | 3 | 19-Sep-14 | 23-Sep-14 | 7 |

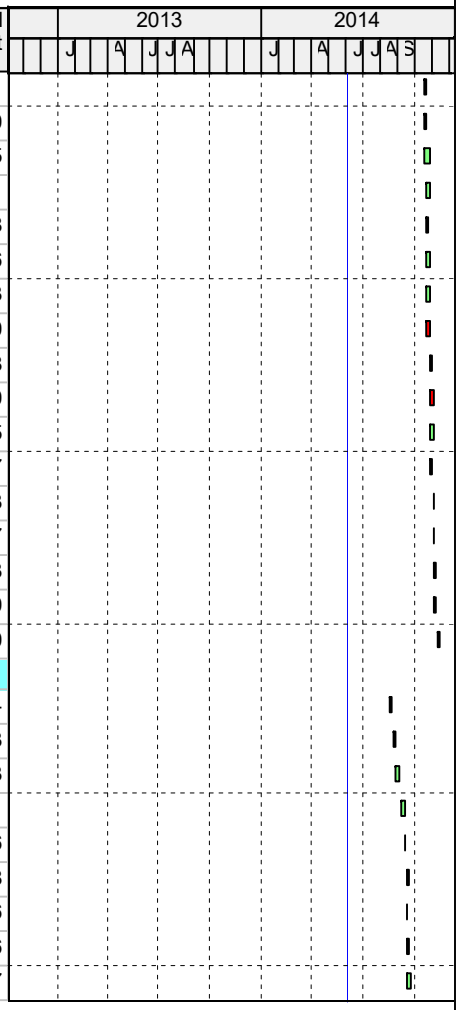


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8214 | LL1 Food Prep Complete | 0 | 0 | | 22-Sep-14 | 46 |
| LL1-8201 | Final Coat Finish Paint | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 11 |
| L1B-8200 | First Coat Finish Paint | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 3 |
| LL1-8204 | Mech Trim / Finish (HVAC & Plumbing) | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 11 |
| LL1-Z2-8201 | Final Coat Finish Paint | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 8 |
| L1L-8200 | First Coat Finish Paint | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 0 |
| L1K-8201 | Final Coat Finish Paint | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 7 |
| LL1-Z2-8204 | Mech Trim / Finish (HVAC & Plumbing) | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 8 |
| L1K-8204 | Mech Trim / Finish (HVAC & Plumbing) | 10 | 10 | 13-Oct-14 | 24-Oct-14 | 7 |
| L1B-8201 | Final Coat Finish Paint | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 3 |
| L1B-8204 | Mech Trim / Finish (HVAC & Plumbing) | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 3 |
| L1L-8201 | Final Coat Finish Paint | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 0 |
| LL1-8210 | Owner Walk / Create Punchlist | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 11 |
| L1L-8204 | Mech Trim / Finish (HVAC & Plumbing) | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 0 |
| LL1-8212 | Final Punchlist | 5 | 5 | 30-Oct-14 | 05-Nov-14 | 11 |
| LL1-Z2-8210 | Owner Walk / Create Punchlist | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 8 |
| LL1-Z2-8212 | Final Punchlist | 5 | 5 | 04-Nov-14 | 11-Nov-14 | 8 |
| LL1-8208 | Final Clean | 3 | 3 | 06-Nov-14 | 11-Nov-14 | 11 |
| L1K-8210 | Owner Walk / Create Punchlist | 1 | 1 | 06-Nov-14 | 06-Nov-14 | 7 |
| L1K-8212 | Final Punchlist | 4 | 4 | 07-Nov-14 | 13-Nov-14 | 7 |
| L1B-8210 | Owner Walk / Create Punchlist | 1 | 1 | 11-Nov-14 | 11-Nov-14 | 3 |
| LL1-8214 | LL1 Meeting /Board Rooms Complete | 0 | 0 | | 11-Nov-14 | 11 |
| LL1-Z2-8208 | Final Clean | 3 | 3 | 12-Nov-14 | 14-Nov-14 | 8 |
| L1B-8212 | Final Punchlist | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 3 |
| L1L-8210 | Owner Walk / Create Punchlist | 1 | 1 | 14-Nov-14 | 14-Nov-14 | 0 |
| L1K-8208 | Final Clean | 2 | 2 | 14-Nov-14 | 17-Nov-14 | 7 |
| LL1-Z2-8214 | LL1 Junior Ballrooms Complete | 0 | 0 | | 14-Nov-14 | 8 |

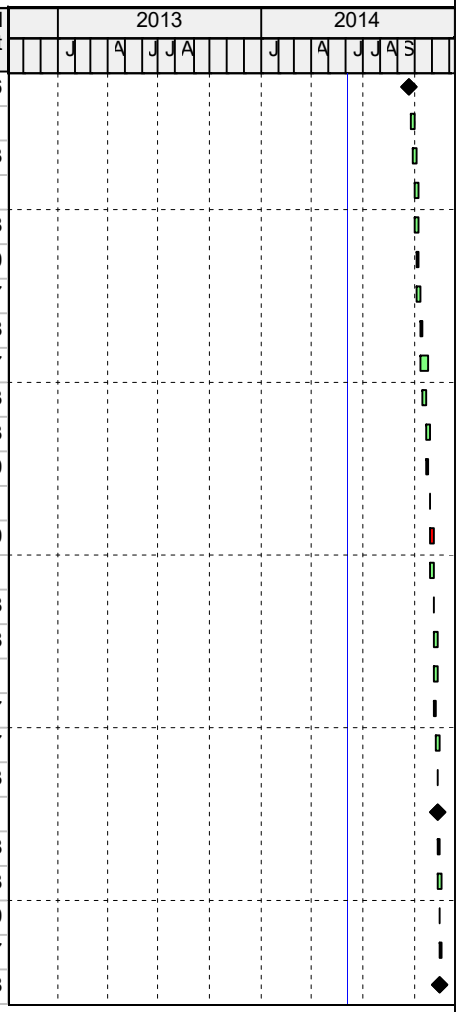


Actual Work | Remaining Work | Critical Remai... | Milestone | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8212 | Final Punchlist | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 0 |
| L1K-8214 | L1 Kitchen Complete | 0 | 0 | | 17-Nov-14 | 7 |
| L1B-8208 | Final Clean | 3 | 3 | 19-Nov-14 | 21-Nov-14 | 3 |
| L1B-8214 | L1 Ballrooms Complete | 0 | 0 | | 21-Nov-14 | 3 |
| L1L-8208 | Final Clean | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 0 |
| L1L-8214 | L1 Common Areas Complete | 0 | 0 | | 26-Nov-14 | 0 |
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8100 | L2 - Insulation | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 6 |
| L02-8102 | L2 - GWB Hang / Tape / Finish - (Including Common / | 15 | 15 | 19-Aug-14 | 09-Sep-14 | 6 |
| L02-8104 | L2 - Int Painting | 10 | 10 | 05-Sep-14 | 18-Sep-14 | 6 |
| L02-8106 | L2 - Wallcoverings | 6 | 6 | 09-Sep-14 | 16-Sep-14 | 18 |
| L02-8116 | L2 - Finish Carpentry / Millwork | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 11 |
| L02-8120 | L2 - Ceramic Tile / Counter Tops | 8 | 8 | 16-Sep-14 | 25-Sep-14 | 11 |
| L02-8122 | L2 - Plumbing Trim / Finish | 8 | 8 | 18-Sep-14 | 29-Sep-14 | 13 |
| L02-8108 | L2 - Elec Trim / Finish | 10 | 10 | 19-Sep-14 | 02-Oct-14 | 6 |
| L02-8110 | L2 - HVAC Trim / Finish | 10 | 10 | 19-Sep-14 | 02-Oct-14 | 6 |
| L02-8112 | L2 - Fire Sprinkler Trim / Finish | 8 | 8 | 19-Sep-14 | 30-Sep-14 | 8 |
| L02-8118 | L2 - Elec Specialties Trim / Finish | 10 | 10 | 19-Sep-14 | 02-Oct-14 | 6 |
| L02-8136 | L2 - Lockers / Benches @ Locker Rooms | 5 | 5 | 19-Sep-14 | 25-Sep-14 | 17 |
| L02-8128 | L2 - Bath Specialties | 2 | 2 | 30-Sep-14 | 01-Oct-14 | 13 |
| L02-8124 | L2 - Flooring | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 6 |
| L02-8126 | L2 - Doors & Hardware | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 6 |
| L02-8130 | L2 - Admin / Employee Rooms Substantially Complet | 0 | 0 | | 10-Oct-14 | 6 |
| L02-8132 | L2 - Contractor Pre-Punchlist | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 21 |
| L02-8134 | L2 - Pre-Clean | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 16 |
| **Corridors** | | | | | | |

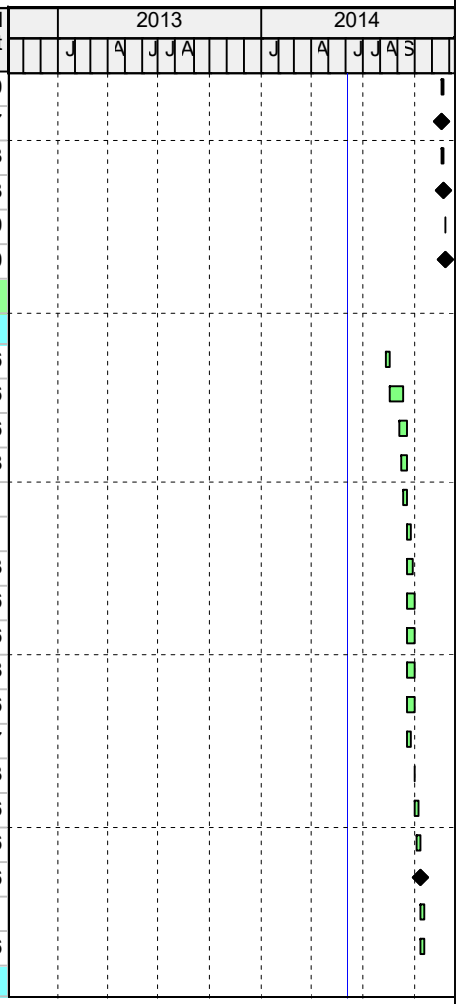



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8200 | L2 - Final Paint @ Common / Public Areas | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 6 |
| L02-8114 | L2 - Signage | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 13 |
| L02-8202 | L2 - Elec Trim / Finish @ Common / Public Areas | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 7 |
| L02-8204 | L2 - Mech Trim / Finish @ Common / Public Areas (H | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 6 |
| L02-8206 | L2 - Flooring @ Corridors | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 6 |
| L02-8208 | L2 - Final Clean | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 6 |
| L02-8210 | L2 - Owner Walk / Create Punchlist | 1 | 1 | 11-Nov-14 | 11-Nov-14 | 6 |
| L02-8212 | L2 - Final Punchlist | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 6 |
| L02-8214 | L2 - Floor Complete | 0 | 0 | | 18-Nov-14 | 6 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L03-8102S | Stock GWB | 2 | 2 | 13-Jun-14 | 16-Jun-14 | 37 |
| L03-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 17-Jun-14 | 25-Jun-14 | 37 |
| L04-8102S | Stock GWB | 2 | 2 | 18-Jun-14 | 19-Jun-14 | 36 |
| L05-8102S | Stock GWB | 2 | 2 | 18-Jun-14 | 19-Jun-14 | 41 |
| L06-8102S | Stock GWB | 2 | 2 | 18-Jun-14 | 19-Jun-14 | 43 |
| L07-8102S | Stock GWB | 2 | 2 | 18-Jun-14 | 19-Jun-14 | 48 |
| L04-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 20-Jun-14 | 30-Jun-14 | 36 |
| L08-8102S | Stock GWB | 2 | 2 | 23-Jun-14 | 24-Jun-14 | 45 |
| L10-8102S | Stock GWB | 2 | 2 | 23-Jun-14 | 24-Jun-14 | 52 |
| L05-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 26-Jun-14 | 07-Jul-14 | 37 |
| L09-8102S | Stock GWB | 2 | 2 | 27-Jun-14 | 30-Jun-14 | 48 |
| L11-8102S | Stock GWB | 2 | 2 | 27-Jun-14 | 30-Jun-14 | 41 |
| L06-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 01-Jul-14 | 10-Jul-14 | 36 |
| L12-8102S | Stock GWB | 2 | 2 | 02-Jul-14 | 03-Jul-14 | 45 |
| L03-8104 | Primer Paint Coat | 2 | 2 | 07-Jul-14 | 08-Jul-14 | 44 |

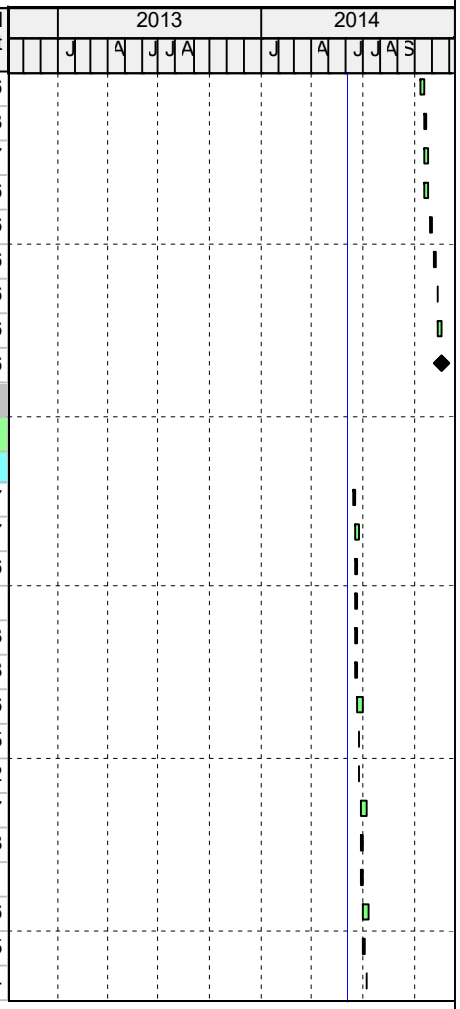



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8116 | Install Wood Base | 3 | 3 | 09-Jul-14 | 11-Jul-14 | 49 |
| L03-8120 | Install Casework/Countertops | 5 | 5 | 09-Jul-14 | 15-Jul-14 | 44 |
| L07-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 09-Jul-14 | 17-Jul-14 | 36 |
| L08-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 09-Jul-14 | 17-Jul-14 | 36 |
| L14-8102S | Stock GWB | 2 | 2 | 09-Jul-14 | 10-Jul-14 | 41 |
| L04-8104 | Primer Paint Coat | 2 | 2 | 10-Jul-14 | 11-Jul-14 | 41 |
| L11-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 10-Jul-14 | 18-Jul-14 | 35 |
| L12-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 10-Jul-14 | 18-Jul-14 | 42 |
| L03-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 14-Jul-14 | 18-Jul-14 | 44 |
| L04-8116 | Install Wood Base | 3 | 3 | 14-Jul-14 | 16-Jul-14 | 46 |
| L04-8120 | Install Casework/Countertops | 5 | 5 | 14-Jul-14 | 18-Jul-14 | 41 |
| L15-8102S | Stock GWB | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 12 |
| L05-8104 | Primer Paint Coat | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 37 |
| L03-8128 | Install Tub Glazing | 4 | 4 | 17-Jul-14 | 22-Jul-14 | 44 |
| L04-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 17-Jul-14 | 23-Jul-14 | 41 |
| L05-8116 | Install Wood Base | 3 | 3 | 18-Jul-14 | 22-Jul-14 | 42 |
| L05-8120 | Install Casework/Countertops | 5 | 5 | 18-Jul-14 | 24-Jul-14 | 37 |
| L09-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 18-Jul-14 | 28-Jul-14 | 36 |
| L10-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 18-Jul-14 | 28-Jul-14 | 36 |
| L15-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 18-Jul-14 | 28-Jul-14 | 10 |
| L03-8105 | First Coat Finish Paint | 5 | 5 | 21-Jul-14 | 25-Jul-14 | 44 |
| L06-8104 | Primer Paint Coat | 2 | 2 | 21-Jul-14 | 22-Jul-14 | 48 |
| L14-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 21-Jul-14 | 29-Jul-14 | 35 |
| L16-8102S | Stock GWB | 2 | 2 | 21-Jul-14 | 22-Jul-14 | 19 |
| L04-8128 | Install Tub Glazing | 4 | 4 | 22-Jul-14 | 25-Jul-14 | 41 |
| L03-8124 | Flooring @ Guest Rooms | 5 | 5 | 23-Jul-14 | 29-Jul-14 | 44 |
| L05-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 23-Jul-14 | 29-Jul-14 | 37 |

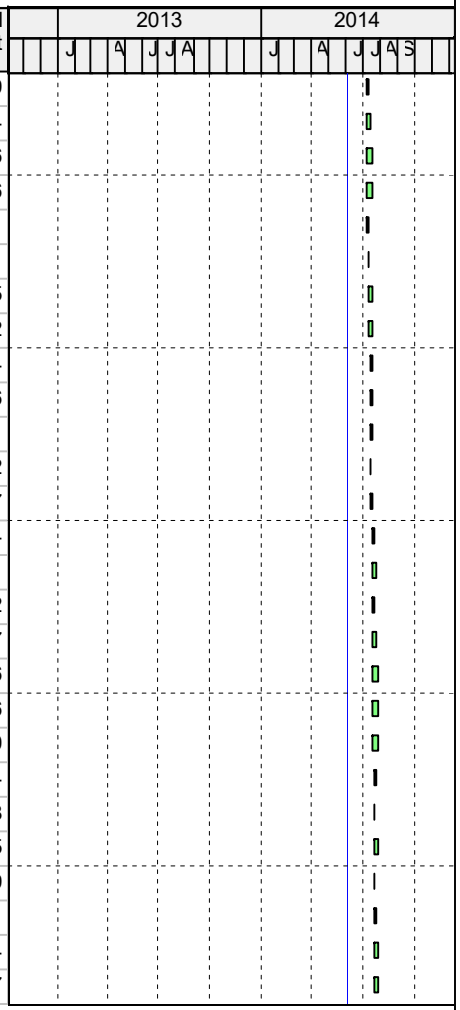



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8116 | Install Wood Base | 3 | 3 | 23-Jul-14 | 25-Jul-14 | 53 |
| L06-8120 | Install Casework/Countertops | 5 | 5 | 23-Jul-14 | 29-Jul-14 | 48 |
| L16-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 23-Jul-14 | 31-Jul-14 | 19 |
| L04-8105 | First Coat Finish Paint | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 41 |
| L17-8102S | Stock GWB | 2 | 2 | 24-Jul-14 | 25-Jul-14 | 11 |
| L04-8124 | Flooring @ Guest Rooms | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 41 |
| L05-8128 | Install Tub Glazing | 4 | 4 | 28-Jul-14 | 31-Jul-14 | 37 |
| L06-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 48 |
| L07-8104 | Primer Paint Coat | 2 | 2 | 28-Jul-14 | 29-Jul-14 | 43 |
| L08-8104 | Primer Paint Coat | 2 | 2 | 28-Jul-14 | 29-Jul-14 | 43 |
| L11-8104 | Primer Paint Coat | 2 | 2 | 29-Jul-14 | 30-Jul-14 | 42 |
| L12-8104 | Primer Paint Coat | 2 | 2 | 29-Jul-14 | 30-Jul-14 | 42 |
| L17-8102 | Hang GWB/Install Sound Batts | 7 | 7 | 29-Jul-14 | 06-Aug-14 | 10 |
| L03-8107 | Final Coat Finish Paint | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 44 |
| L05-8105 | First Coat Finish Paint | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 37 |
| L07-8116 | Install Wood Base | 3 | 3 | 30-Jul-14 | 01-Aug-14 | 48 |
| L07-8120 | Install Casework/Countertops | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 43 |
| L08-8116 | Install Wood Base | 3 | 3 | 30-Jul-14 | 01-Aug-14 | 48 |
| L08-8120 | Install Casework/Countertops | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 43 |
| L06-8128 | Install Tub Glazing | 4 | 4 | 31-Jul-14 | 05-Aug-14 | 48 |
| L11-8116 | Install Wood Base | 3 | 3 | 31-Jul-14 | 04-Aug-14 | 47 |
| L11-8120 | Install Casework/Countertops | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 42 |
| L12-8116 | Install Wood Base | 3 | 3 | 31-Jul-14 | 04-Aug-14 | 47 |
| L12-8120 | Install Casework/Countertops | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 42 |
| L05-8124 | Flooring @ Guest Rooms | 5 | 5 | 01-Aug-14 | 07-Aug-14 | 37 |
| L03-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 62 |
| L03-8108 | Elec Trim / Finish | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 44 |

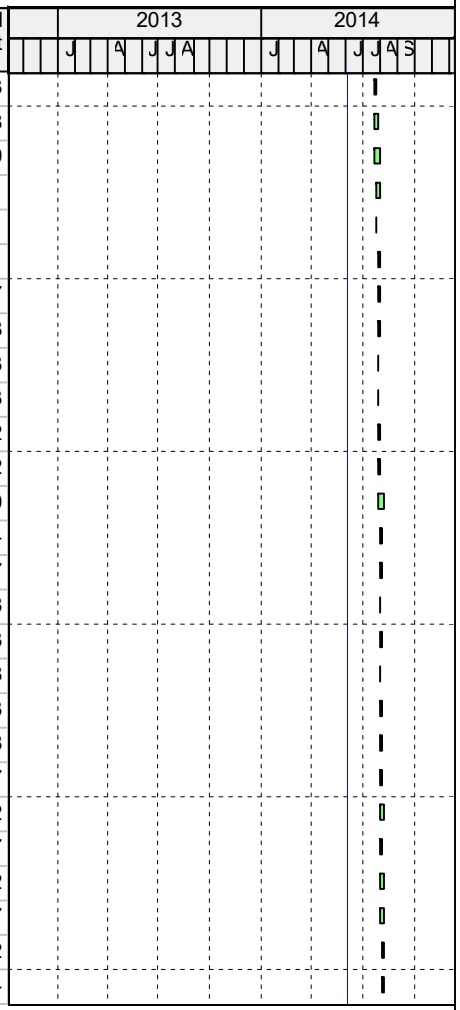



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8110 | HVAC Trim / Finish | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 44 |
| L03-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 44 |
| L04-8107 | Final Coat Finish Paint | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 41 |
| L06-8105 | First Coat Finish Paint | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 48 |
| L07-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 43 |
| L08-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 43 |
| L11-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 42 |
| L12-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 42 |
| L03-8126 | Doors & Hardware | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 58 |
| L03-8118 | Elec Specialties Trim / Finish | 4 | 4 | 06-Aug-14 | 11-Aug-14 | 61 |
| L06-8124 | Flooring @ Guest Rooms | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 48 |
| L09-8104 | Primer Paint Coat | 2 | 2 | 06-Aug-14 | 07-Aug-14 | 36 |
| L10-8104 | Primer Paint Coat | 2 | 2 | 06-Aug-14 | 07-Aug-14 | 36 |
| L15-8104 | Primer Paint Coat | 2 | 2 | 06-Aug-14 | 07-Aug-14 | 22 |
| L04-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 59 |
| L04-8108 | Elec Trim / Finish | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 41 |
| L04-8110 | HVAC Trim / Finish | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 41 |
| L04-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 41 |
| L07-8128 | Install Tub Glazing | 4 | 4 | 07-Aug-14 | 12-Aug-14 | 43 |
| L08-8128 | Install Tub Glazing | 4 | 4 | 07-Aug-14 | 12-Aug-14 | 43 |
| L14-8104 | Primer Paint Coat | 2 | 2 | 07-Aug-14 | 08-Aug-14 | 35 |
| L03-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 08-Aug-14 | 12-Aug-14 | 60 |
| L05-8107 | Final Coat Finish Paint | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 37 |
| L09-8116 | Install Wood Base | 3 | 3 | 08-Aug-14 | 12-Aug-14 | 41 |
| L09-8120 | Install Casework/Countertops | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 36 |
| L10-8116 | Install Wood Base | 3 | 3 | 08-Aug-14 | 12-Aug-14 | 41 |
| L10-8120 | Install Casework/Countertops | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 36 |

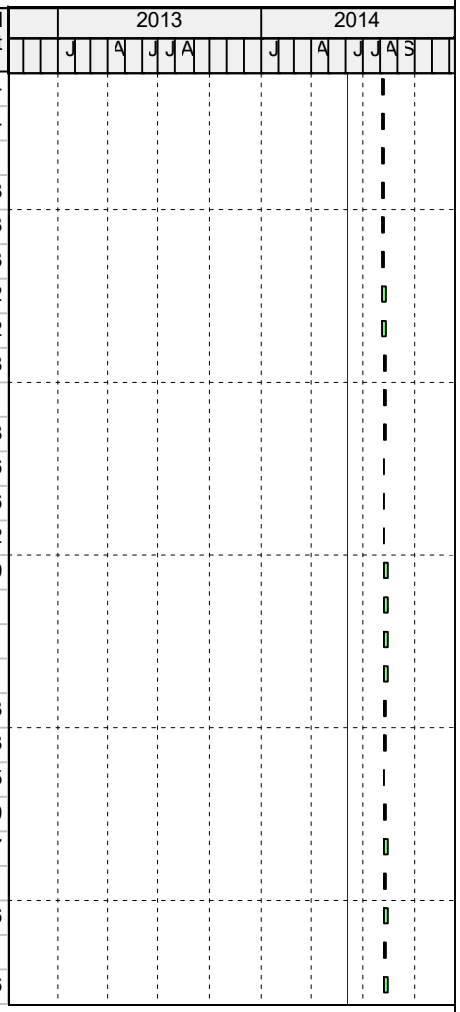



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8128 | Install Tub Glazing | 4 | 4 | 08-Aug-14 | 13-Aug-14 | 42 |
| L12-8128 | Install Tub Glazing | 4 | 4 | 08-Aug-14 | 13-Aug-14 | 42 |
| L15-8116 | Install Wood Base | 3 | 3 | 08-Aug-14 | 12-Aug-14 | 27 |
| L15-8120 | Install Casework/Countertops | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 22 |
| L04-8126 | Doors & Hardware | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 55 |
| L04-8118 | Elec Specialties Trim / Finish | 4 | 4 | 11-Aug-14 | 14-Aug-14 | 58 |
| L07-8105 | First Coat Finish Paint | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 43 |
| L08-8105 | First Coat Finish Paint | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 43 |
| L14-8116 | Install Wood Base | 3 | 3 | 11-Aug-14 | 13-Aug-14 | 40 |
| L14-8120 | Install Casework/Countertops | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 35 |
| L16-8104 | Primer Paint Coat | 2 | 2 | 11-Aug-14 | 12-Aug-14 | 19 |
| L03-8114 | Signage (By Owner) | 3 | 3 | 12-Aug-14 | 14-Aug-14 | 58 |
| L11-8105 | First Coat Finish Paint | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 42 |
| L12-8105 | First Coat Finish Paint | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 42 |
| L04-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 13-Aug-14 | 15-Aug-14 | 57 |
| L05-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 55 |
| L05-8108 | Elec Trim / Finish | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 37 |
| L05-8110 | HVAC Trim / Finish | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 37 |
| L05-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 37 |
| L06-8107 | Final Coat Finish Paint | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 48 |
| L07-8124 | Flooring @ Guest Rooms | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 43 |
| L08-8124 | Flooring @ Guest Rooms | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 43 |
| L09-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 36 |
| L10-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 36 |
| L15-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 22 |
| L16-8116 | Install Wood Base | 3 | 3 | 13-Aug-14 | 15-Aug-14 | 24 |
| L16-8120 | Install Casework/Countertops | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 19 |

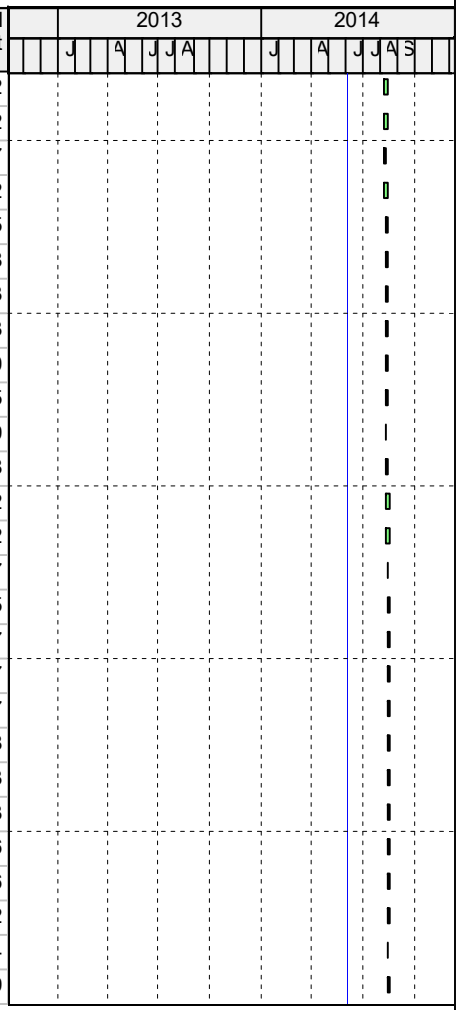



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8124 | Flooring @ Guest Rooms | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 42 |
| L12-8124 | Flooring @ Guest Rooms | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 42 |
| L14-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 35 |
| L04-8114 | Signage (By Owner) | 3 | 3 | 15-Aug-14 | 19-Aug-14 | 55 |
| L05-8126 | Doors & Hardware | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 51 |
| L05-8118 | Elec Specialties Trim / Finish | 4 | 4 | 15-Aug-14 | 20-Aug-14 | 54 |
| L06-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 52 |
| L06-8108 | Elec Trim / Finish | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 52 |
| L06-8110 | HVAC Trim / Finish | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 52 |
| L06-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 52 |
| L09-8128 | Install Tub Glazing | 4 | 4 | 18-Aug-14 | 21-Aug-14 | 36 |
| L10-8128 | Install Tub Glazing | 4 | 4 | 18-Aug-14 | 21-Aug-14 | 36 |
| L15-8128 | Install Tub Glazing | 4 | 4 | 18-Aug-14 | 21-Aug-14 | 22 |
| L16-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 19 |
| L05-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 19-Aug-14 | 21-Aug-14 | 53 |
| L14-8128 | Install Tub Glazing | 4 | 4 | 19-Aug-14 | 22-Aug-14 | 35 |
| L06-8126 | Doors & Hardware | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 48 |
| L06-8118 | Elec Specialties Trim / Finish | 4 | 4 | 20-Aug-14 | 25-Aug-14 | 51 |
| L07-8107 | Final Coat Finish Paint | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 43 |
| L08-8107 | Final Coat Finish Paint | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 43 |
| L09-8105 | First Coat Finish Paint | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 36 |
| L10-8105 | First Coat Finish Paint | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 36 |
| L15-8105 | First Coat Finish Paint | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 22 |
| L05-8114 | Signage (By Owner) | 3 | 3 | 21-Aug-14 | 25-Aug-14 | 51 |
| L11-8107 | Final Coat Finish Paint | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 42 |
| L12-8107 | Final Coat Finish Paint | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 42 |
| L14-8105 | First Coat Finish Paint | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 35 |





© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8128 | Install Tub Glazing | 4 | 4 | 21-Aug-14 | 26-Aug-14 | 19 |
| L06-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 22-Aug-14 | 26-Aug-14 | 50 |
| L09-8124 | Flooring @ Guest Rooms | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 36 |
| L10-8124 | Flooring @ Guest Rooms | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 36 |
| L15-8124 | Flooring @ Guest Rooms | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 22 |
| L17-8104 | Primer Paint Coat | 2 | 2 | 22-Aug-14 | 25-Aug-14 | 10 |
| L07-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 47 |
| L07-8108 | Elec Trim / Finish | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 47 |
| L07-8110 | HVAC Trim / Finish | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 47 |
| L07-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 47 |
| L08-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 47 |
| L08-8108 | Elec Trim / Finish | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 47 |
| L08-8110 | HVAC Trim / Finish | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 47 |
| L08-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 47 |
| L14-8124 | Flooring @ Guest Rooms | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 35 |
| L16-8105 | First Coat Finish Paint | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 19 |
| L03-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 25-Aug-14 | 51 |
| L04-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 25-Aug-14 | 51 |
| L05-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 25-Aug-14 | 51 |
| L03-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 54 |
| L03-8134 | Pre-Clean Guestrooms | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 51 |
| L04-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 54 |
| L04-8134 | Pre-Clean Guestrooms | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 51 |
| L05-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 54 |
| L05-8134 | Pre-Clean Guestrooms | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 51 |
| L06-8114 | Signage (By Owner) | 3 | 3 | 26-Aug-14 | 28-Aug-14 | 48 |
| L11-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 46 |

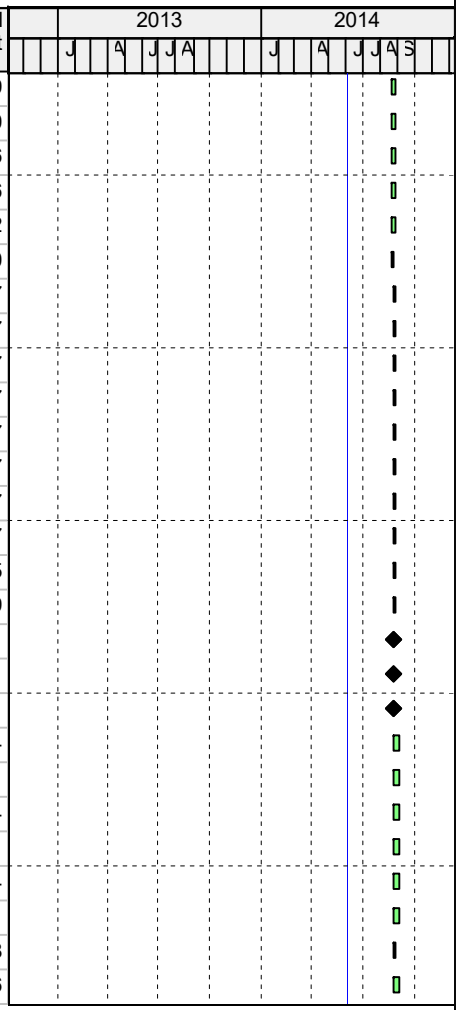



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8108 | Elec Trim / Finish | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 46 |
| L11-8110 | HVAC Trim / Finish | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 46 |
| L11-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 46 |
| L12-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 46 |
| L12-8108 | Elec Trim / Finish | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 46 |
| L12-8110 | HVAC Trim / Finish | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 46 |
| L12-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 46 |
| L17-8116 | Install Wood Base | 3 | 3 | 26-Aug-14 | 28-Aug-14 | 15 |
| L17-8120 | Install Casework/Countertops | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 10 |
| L07-8126 | Doors & Hardware | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 43 |
| L07-8118 | Elec Specialties Trim / Finish | 4 | 4 | 27-Aug-14 | 02-Sep-14 | 46 |
| L08-8126 | Doors & Hardware | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 43 |
| L08-8118 | Elec Specialties Trim / Finish | 4 | 4 | 27-Aug-14 | 02-Sep-14 | 46 |
| L16-8124 | Flooring @ Guest Rooms | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 19 |
| L11-8126 | Doors & Hardware | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 42 |
| L11-8118 | Elec Specialties Trim / Finish | 4 | 4 | 28-Aug-14 | 03-Sep-14 | 45 |
| L12-8126 | Doors & Hardware | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 42 |
| L12-8118 | Elec Specialties Trim / Finish | 4 | 4 | 28-Aug-14 | 03-Sep-14 | 45 |
| L07-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 29-Aug-14 | 03-Sep-14 | 45 |
| L08-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 29-Aug-14 | 03-Sep-14 | 45 |
| L09-8107 | Final Coat Finish Paint | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 36 |
| L10-8107 | Final Coat Finish Paint | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 36 |
| L15-8107 | Final Coat Finish Paint | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 22 |
| L17-8125 | Ceramic Tile @ Bathrooms | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 10 |
| L11-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 02-Sep-14 | 04-Sep-14 | 44 |
| L12-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 02-Sep-14 | 04-Sep-14 | 63 |
| L14-8107 | Final Coat Finish Paint | 5 | 5 | 02-Sep-14 | 08-Sep-14 | 35 |





© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8114 | Signage (By Owner) | 3 | 3 | 03-Sep-14 | 05-Sep-14 | 43 |
| L08-8114 | Signage (By Owner) | 3 | 3 | 03-Sep-14 | 05-Sep-14 | 43 |
| L06-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 03-Sep-14 | 45 |
| L06-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 48 |
| L06-8134 | Pre-Clean Guestrooms | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 45 |
| L09-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 40 |
| L09-8108 | Elec Trim / Finish | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 40 |
| L09-8110 | HVAC Trim / Finish | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 40 |
| L09-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 40 |
| L10-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 40 |
| L10-8108 | Elec Trim / Finish | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 40 |
| L10-8110 | HVAC Trim / Finish | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 40 |
| L10-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 40 |
| L11-8114 | Signage (By Owner) | 3 | 3 | 04-Sep-14 | 08-Sep-14 | 42 |
| L12-8114 | Signage (By Owner) | 3 | 3 | 04-Sep-14 | 08-Sep-14 | 42 |
| L15-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 40 |
| L15-8108 | Elec Trim / Finish | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 22 |
| L15-8110 | HVAC Trim / Finish | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 22 |
| L15-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 22 |
| L16-8107 | Final Coat Finish Paint | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 19 |
| L17-8128 | Install Tub Glazing | 4 | 4 | 04-Sep-14 | 09-Sep-14 | 10 |
| L14-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 05-Sep-14 | 11-Sep-14 | 39 |
| L14-8108 | Elec Trim / Finish | 5 | 5 | 05-Sep-14 | 11-Sep-14 | 39 |
| L14-8110 | HVAC Trim / Finish | 5 | 5 | 05-Sep-14 | 11-Sep-14 | 39 |
| L14-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 05-Sep-14 | 11-Sep-14 | 39 |
| L09-8126 | Doors & Hardware | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 36 |
| L09-8118 | Elec Specialties Trim / Finish | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 39 |

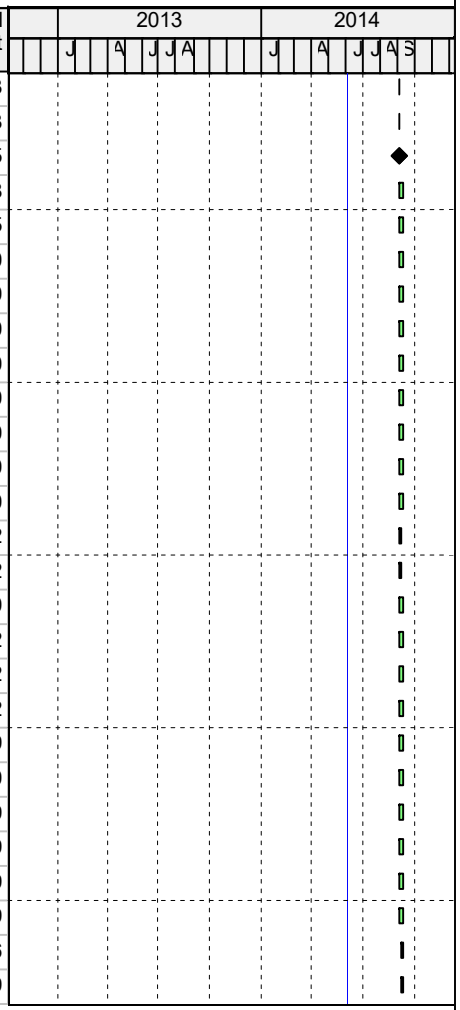



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8126 | Doors & Hardware | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 36 |
| L10-8118 | Elec Specialties Trim / Finish | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 39 |
| L15-8126 | Doors & Hardware | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 36 |
| L15-8118 | Elec Specialties Trim / Finish | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 39 |
| L17-8105 | First Coat Finish Paint | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 10 |
| L14-8126 | Doors & Hardware | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 35 |
| L14-8118 | Elec Specialties Trim / Finish | 4 | 4 | 09-Sep-14 | 12-Sep-14 | 38 |
| L16-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 37 |
| L16-8108 | Elec Trim / Finish | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 19 |
| L16-8110 | HVAC Trim / Finish | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 37 |
| L16-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 19 |
| L09-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 10-Sep-14 | 12-Sep-14 | 38 |
| L10-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 10-Sep-14 | 12-Sep-14 | 38 |
| L15-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 10-Sep-14 | 12-Sep-14 | 38 |
| L17-8124 | Flooring @ Guest Rooms | 5 | 5 | 10-Sep-14 | 16-Sep-14 | 10 |
| L14-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 11-Sep-14 | 15-Sep-14 | 37 |
| L16-8126 | Doors & Hardware | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 33 |
| L16-8118 | Elec Specialties Trim / Finish | 4 | 4 | 11-Sep-14 | 16-Sep-14 | 36 |
| L07-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 11-Sep-14 | 39 |
| L08-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 11-Sep-14 | 39 |
| L07-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 42 |
| L07-8134 | Pre-Clean Guestrooms | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 39 |
| L08-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 42 |
| L08-8134 | Pre-Clean Guestrooms | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 39 |
| L09-8114 | Signage (By Owner) | 3 | 3 | 12-Sep-14 | 16-Sep-14 | 36 |
| L10-8114 | Signage (By Owner) | 3 | 3 | 12-Sep-14 | 16-Sep-14 | 36 |
| L15-8114 | Signage (By Owner) | 3 | 3 | 12-Sep-14 | 16-Sep-14 | 36 |

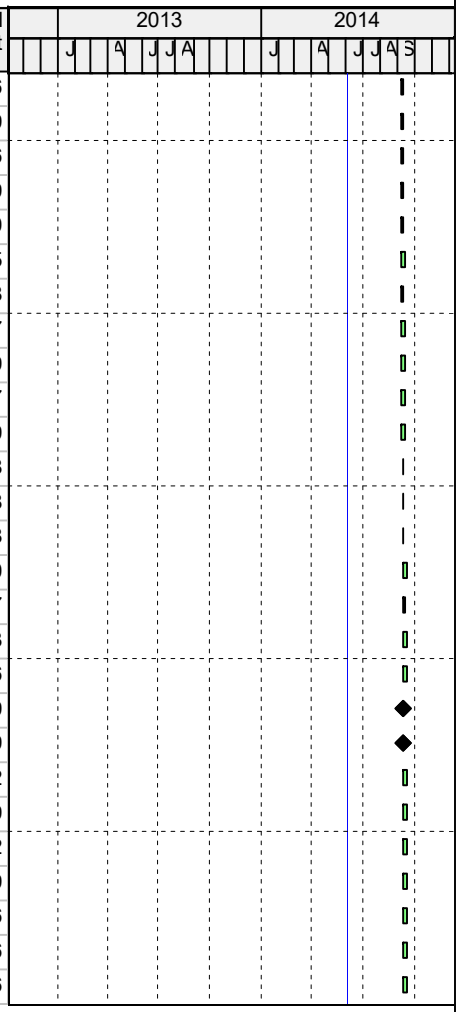



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8114 | Signage (By Owner) | 3 | 3 | 15-Sep-14 | 17-Sep-14 | 35 |
| L16-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 15-Sep-14 | 17-Sep-14 | 35 |
| L15-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 16-Sep-14 | 36 |
| L15-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 39 |
| L15-8134 | Pre-Clean Guestrooms | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 36 |
| L16-8114 | Signage (By Owner) | 3 | 3 | 17-Sep-14 | 19-Sep-14 | 33 |
| L17-8107 | Final Coat Finish Paint | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 10 |
| L09-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 19-Sep-14 | 33 |
| L10-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 19-Sep-14 | 33 |
| L09-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 36 |
| L09-8134 | Pre-Clean Guestrooms | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 33 |
| L10-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 36 |
| L10-8134 | Pre-Clean Guestrooms | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 33 |
| L17-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 28 |
| L17-8108 | Elec Trim / Finish | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 10 |
| L17-8110 | HVAC Trim / Finish | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 10 |
| L17-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 10 |
| L17-8126 | Doors & Hardware | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 24 |
| L17-8118 | Elec Specialties Trim / Finish | 4 | 4 | 24-Sep-14 | 29-Sep-14 | 27 |
| L17-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 26-Sep-14 | 30-Sep-14 | 26 |
| L11-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 29-Sep-14 | 27 |
| L12-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 29-Sep-14 | 27 |
| L11-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 30 |
| L11-8134 | Pre-Clean Guestrooms | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 27 |
| L12-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 30 |
| L12-8134 | Pre-Clean Guestrooms | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 27 |
| L17-8114 | Signage (By Owner) | 3 | 3 | 30-Sep-14 | 02-Oct-14 | 24 |

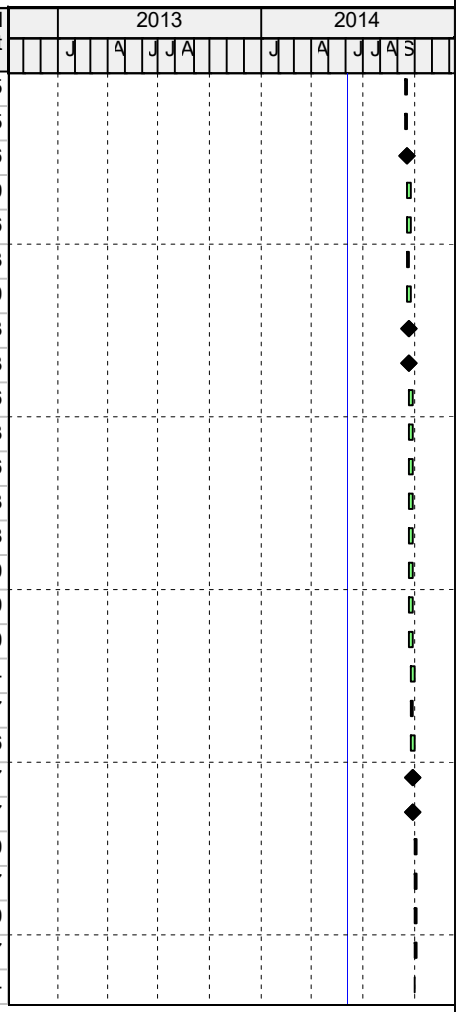



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 07-Oct-14 | 21 |
| L14-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 08-Oct-14 | 14-Oct-14 | 24 |
| L14-8134 | Pre-Clean Guestrooms | 5 | 5 | 08-Oct-14 | 14-Oct-14 | 21 |
| L16-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 15-Oct-14 | 15 |
| L17-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 15-Oct-14 | 15 |
| L16-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 18 |
| L16-8134 | Pre-Clean Guestrooms | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 15 |
| L17-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 18 |
| L17-8134 | Pre-Clean Guestrooms | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 15 |
| **Pool Area** | | | | | | |
| L03-8216 | L3 - Pool Surfaces / Finishes / Accessories | 16 | 16 | 08-Sep-14 | 29-Sep-14 | 31 |
| L03-8218 | L3 - Pool Equipment | 10 | 10 | 30-Sep-14 | 13-Oct-14 | 31 |
| **Corridors / Common / Public Areas** | | | | | | |
| L03-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 60 |
| L03-8206 | Flooring @ Corridors | 2 | 2 | 30-Jul-14 | 31-Jul-14 | 44 |
| L04-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 57 |
| L04-8206 | Flooring @ Corridors | 2 | 2 | 04-Aug-14 | 05-Aug-14 | 41 |
| L03-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 06-Aug-14 | 07-Aug-14 | 60 |
| L03-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 06-Aug-14 | 07-Aug-14 | 60 |
| L05-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 53 |
| L05-8206 | Flooring @ Corridors | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 37 |
| L04-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 11-Aug-14 | 12-Aug-14 | 57 |
| L04-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 11-Aug-14 | 12-Aug-14 | 57 |
| L06-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 50 |
| L06-8206 | Flooring @ Corridors | 2 | 2 | 13-Aug-14 | 14-Aug-14 | 48 |
| L05-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 15-Aug-14 | 18-Aug-14 | 53 |
| L05-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 15-Aug-14 | 18-Aug-14 | 53 |

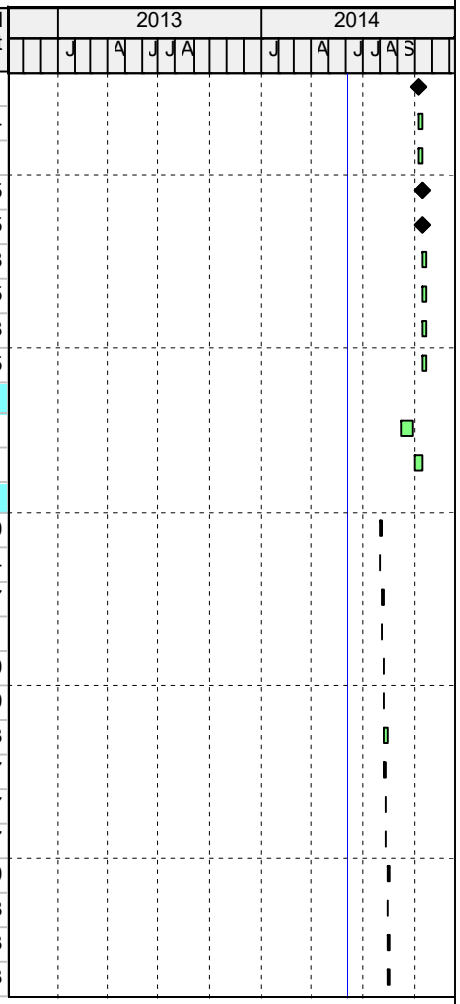



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 20-Aug-14 | 21-Aug-14 | 50 |
| L06-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 20-Aug-14 | 21-Aug-14 | 50 |
| L07-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 45 |
| L07-8206 | Flooring @ Corridors | 2 | 2 | 20-Aug-14 | 21-Aug-14 | 43 |
| L08-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 45 |
| L08-8206 | Flooring @ Corridors | 2 | 2 | 20-Aug-14 | 21-Aug-14 | 43 |
| L11-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 44 |
| L11-8206 | Flooring @ Corridors | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 42 |
| L12-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 46 |
| L12-8206 | Flooring @ Corridors | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 42 |
| L07-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 45 |
| L07-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 45 |
| L08-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 45 |
| L08-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 45 |
| L11-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 28-Aug-14 | 29-Aug-14 | 44 |
| L11-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 28-Aug-14 | 29-Aug-14 | 44 |
| L12-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 28-Aug-14 | 29-Aug-14 | 47 |
| L12-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 28-Aug-14 | 29-Aug-14 | 47 |
| L09-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 38 |
| L09-8206 | Flooring @ Corridors | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 36 |
| L10-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 38 |
| L10-8206 | Flooring @ Corridors | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 36 |
| L15-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 38 |
| L15-8206 | Flooring @ Corridors | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 22 |
| L14-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 02-Sep-14 | 08-Sep-14 | 37 |
| L14-8206 | Flooring @ Corridors | 2 | 2 | 02-Sep-14 | 03-Sep-14 | 35 |
| L03-8208 | Final Clean | 3 | 3 | 03-Sep-14 | 05-Sep-14 | 51 |

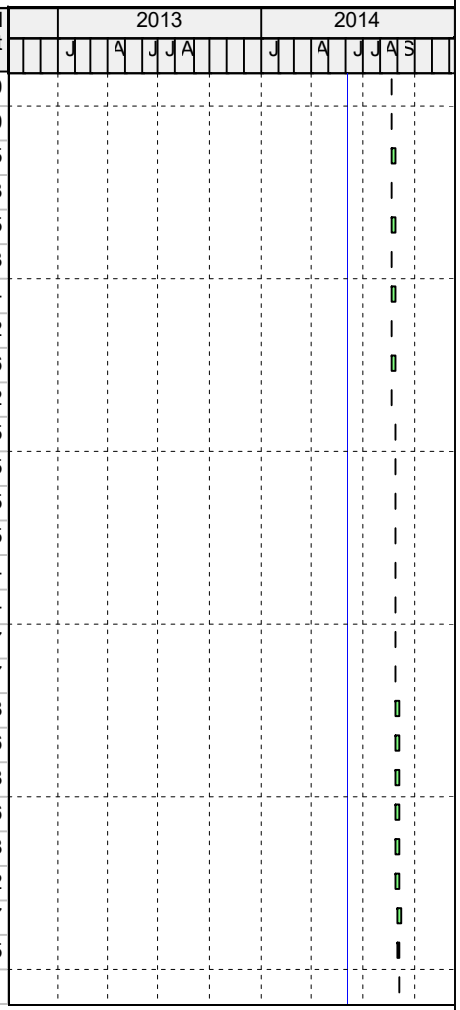



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8208 | Final Clean | 3 | 3 | 03-Sep-14 | 05-Sep-14 | 51 |
| L05-8208 | Final Clean | 3 | 3 | 03-Sep-14 | 05-Sep-14 | 51 |
| L16-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 35 |
| L16-8206 | Flooring @ Corridors | 2 | 2 | 04-Sep-14 | 05-Sep-14 | 19 |
| L03-8210 | Owner Walk / Create Punchlist | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 51 |
| L04-8210 | Owner Walk / Create Punchlist | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 51 |
| L05-8210 | Owner Walk / Create Punchlist | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 51 |
| L09-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 38 |
| L09-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 38 |
| L10-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 38 |
| L10-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 38 |
| L15-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 38 |
| L15-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 38 |
| L03-8212 | Resolve Final Punchlist | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 51 |
| L04-8212 | Resolve Final Punchlist | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 51 |
| L05-8212 | Resolve Final Punchlist | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 51 |
| L14-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 37 |
| L14-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 37 |
| L06-8208 | Final Clean | 3 | 3 | 11-Sep-14 | 15-Sep-14 | 45 |
| L16-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 35 |
| L16-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 35 |
| L04-8214 | Floor Complete | 0 | 0 | | 15-Sep-14 | 51 |
| L05-8214 | Floor Complete | 0 | 0 | | 15-Sep-14 | 51 |
| L06-8210 | Owner Walk / Create Punchlist | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 45 |
| L06-8212 | Resolve Final Punchlist | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 45 |
| L17-8200 | Vinyl Wall Coverings @ Bathrooms/Corridors | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 26 |
| L17-8206 | Flooring @ Corridors | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 10 |

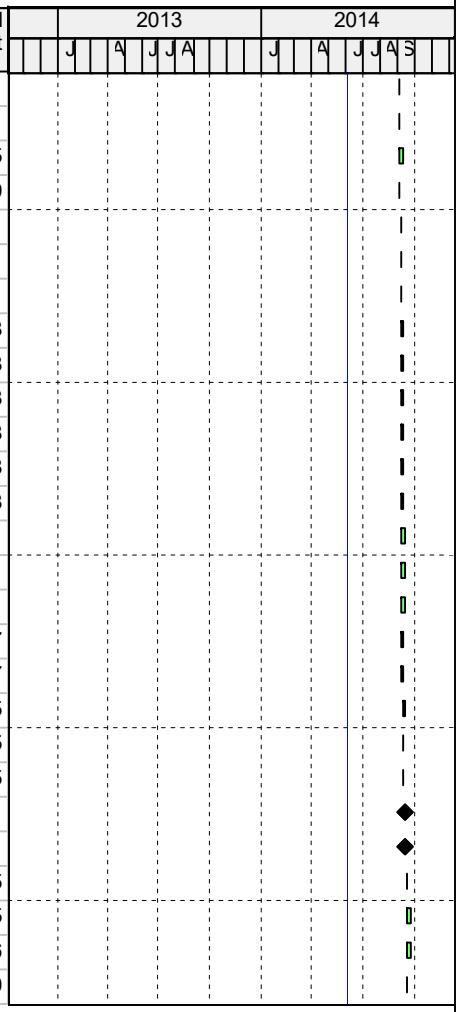


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8208 | Final Clean | 3 | 3 | 19-Sep-14 | 23-Sep-14 | 39 |
| L08-8208 | Final Clean | 3 | 3 | 19-Sep-14 | 23-Sep-14 | 39 |
| L06-8214 | Floor Complete | 0 | 0 | | 23-Sep-14 | 45 |
| L07-8210 | Owner Walk / Create Punchlist | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 39 |
| L08-8210 | Owner Walk / Create Punchlist | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 39 |
| L15-8208 | Final Clean | 3 | 3 | 24-Sep-14 | 26-Sep-14 | 36 |
| L17-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 26 |
| L17-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 26 |
| L03-8214 | Floor Complete | 0 | 0 | | 24-Sep-14 | 44 |
| L07-8212 | Resolve Final Punchlist | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 39 |
| L08-8212 | Resolve Final Punchlist | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 39 |
| L09-8208 | Final Clean | 3 | 3 | 29-Sep-14 | 01-Oct-14 | 33 |
| L10-8208 | Final Clean | 3 | 3 | 29-Sep-14 | 01-Oct-14 | 33 |
| L15-8210 | Owner Walk / Create Punchlist | 1 | 1 | 29-Sep-14 | 29-Sep-14 | 36 |
| L15-8212 | Resolve Final Punchlist | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 36 |
| L07-8214 | Floor Complete | 0 | 0 | | 01-Oct-14 | 39 |
| L08-8214 | Floor Complete | 0 | 0 | | 01-Oct-14 | 39 |
| L09-8210 | Owner Walk / Create Punchlist | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 33 |
| L10-8210 | Owner Walk / Create Punchlist | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 33 |
| L09-8212 | Resolve Final Punchlist | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 33 |
| L10-8212 | Resolve Final Punchlist | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 33 |
| L15-8214 | Floor Complete | 0 | 0 | | 06-Oct-14 | 36 |
| L11-8208 | Final Clean | 3 | 3 | 07-Oct-14 | 09-Oct-14 | 27 |
| L12-8208 | Final Clean | 3 | 3 | 07-Oct-14 | 09-Oct-14 | 27 |
| L09-8214 | Floor Complete | 0 | 0 | | 09-Oct-14 | 33 |
| L10-8214 | Floor Complete | 0 | 0 | | 09-Oct-14 | 33 |
| L11-8210 | Owner Walk / Create Punchlist | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 27 |

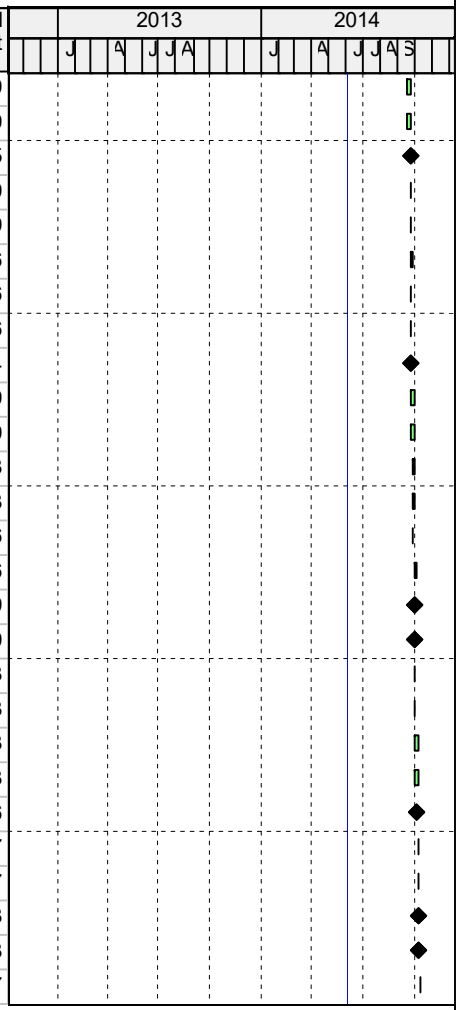


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8210 | Owner Walk / Create Punchlist | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 27 |
| L11-8212 | Resolve Final Punchlist | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 27 |
| L12-8212 | Resolve Final Punchlist | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 27 |
| L14-8208 | Final Clean | 3 | 3 | 15-Oct-14 | 17-Oct-14 | 21 |
| L11-8214 | Floor Complete | 0 | 0 | | 17-Oct-14 | 27 |
| L12-8214 | Floor Complete | 0 | 0 | | 17-Oct-14 | 27 |
| L14-8210 | Owner Walk / Create Punchlist | 1 | 1 | 20-Oct-14 | 20-Oct-14 | 21 |
| L14-8212 | Resolve Final Punchlist | 5 | 5 | 21-Oct-14 | 27-Oct-14 | 21 |
| L16-8208 | Final Clean | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 15 |
| L17-8208 | Final Clean | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 15 |
| L14-8214 | Floor Complete | 0 | 0 | | 27-Oct-14 | 21 |
| L16-8210 | Owner Walk / Create Punchlist | 1 | 1 | 28-Oct-14 | 28-Oct-14 | 15 |
| L17-8210 | Owner Walk / Create Punchlist | 1 | 1 | 28-Oct-14 | 28-Oct-14 | 15 |
| L16-8212 | Resolve Final Punchlist | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 15 |
| L17-8212 | Resolve Final Punchlist | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 15 |
| L16-8214 | Floor Complete | 0 | 0 | | 04-Nov-14 | 15 |
| L17-8214 | Floor Complete | 0 | 0 | | 04-Nov-14 | 15 |
| **Mech Penthouse** | | | | | | |
| PH-8100 | PH - Insulation | 3 | 3 | 14-Aug-14 | 18-Aug-14 | 10 |
| PH-8102 | PH - GWB Hang / Tape / Finish - (Including Common | 10 | 10 | 19-Aug-14 | 02-Sep-14 | 10 |
| PH-8104 | PH - Int Painting | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 10 |
| PH-8122 | PH - Plumbing Trim / Finish | 10 | 10 | 09-Sep-14 | 22-Sep-14 | 10 |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 5 | 5 | 10-Sep-14 | 16-Sep-14 | 28 |
| PH-8114 | PH - Signage | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 44 |
| PH-8108 | PH - Elec Trim / Finish | 10 | 10 | 23-Sep-14 | 06-Oct-14 | 10 |
| PH-8110 | PH - HVAC Trim / Finish | 10 | 10 | 23-Sep-14 | 06-Oct-14 | 14 |
| PH-8118 | PH - Elec Specialties Trim / Finish | 4 | 4 | 07-Oct-14 | 10-Oct-14 | 10 |

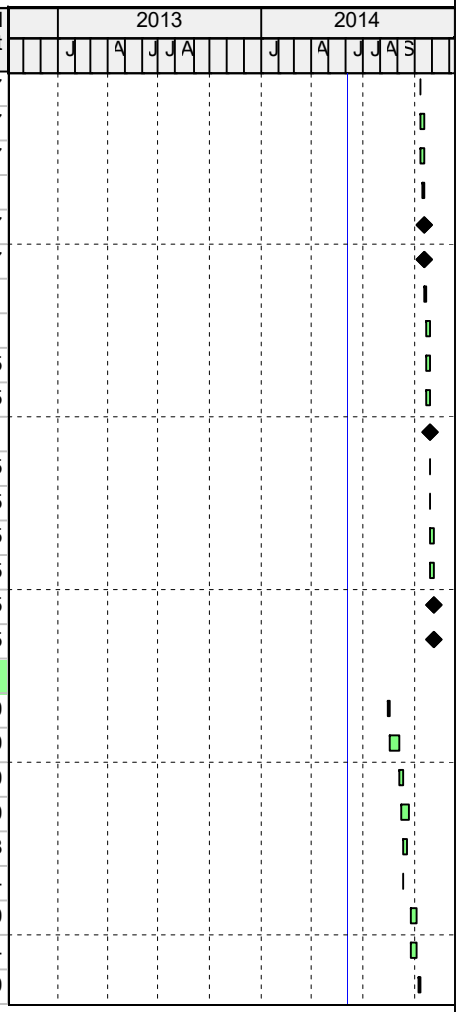


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-8124 | PH - Flooring | 4 | 4 | 13-Oct-14 | 16-Oct-14 | 10 |
| PH-8126 | PH - Doors & Hardware | 3 | 3 | 15-Oct-14 | 17-Oct-14 | 10 |
| PH-8134 | PH - Pre-Clean | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 10 |
| PH-8132 | PH - Contractor Pre-Punchlist | 5 | 5 | 23-Oct-14 | 29-Oct-14 | 10 |
| PH-8208 | PH - Final Clean | 3 | 3 | 30-Oct-14 | 03-Nov-14 | 10 |
| PH-8210 | PH - Owner Walk / Create Punchlist | 1 | 1 | 04-Nov-14 | 04-Nov-14 | 10 |
| PH-8212 | PH - Final Punchlist | 5 | 5 | 05-Nov-14 | 12-Nov-14 | 10 |
| PH-8214 | PH - Floor Complete | 0 | 0 | | 12-Nov-14 | 10 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| **Smoke Control** | | | | | | |
| CO-7104 | Smoke Control Pre-Testing (Podium) | 5 | 5 | 05-Nov-14 | 12-Nov-14 | 5 |
| CO-7106 | City of Bellevue Smoke Control Testing (Podium) | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 5 |
| CO-7108 | Final Marriott Smoke Control Testing | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 5 |
| **Fire Sprinklers** | | | | | | |
| CO-7110 | Fire Sprinkler Pre-Testing (Podium) | 5 | 5 | 05-Nov-14 | 12-Nov-14 | 5 |
| CO-7112 | City of Bellevue Fire Sprinkler Inspection / Approval (F | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 5 |
| CO-7114 | Marriott Fire Sprinkler Testing | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 5 |
| **Fire Alarm** | | | | | | |
| CO-7116 | Fire Alarm Pre-Testing (Podium) | 5 | 5 | 05-Nov-14 | 12-Nov-14 | 5 |
| CO-7118 | City of Bellevue Fire Alarm Inspection / Approval (Pod | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 5 |
| CO-7120 | Marriott Fire Alarm Testing | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 5 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| CO-7100 | CO - Preliminary Start-Up & Testing (Podium) | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 7 |
| CO-7102 | CO - HVAC Commissioning (Podium) | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 12 |

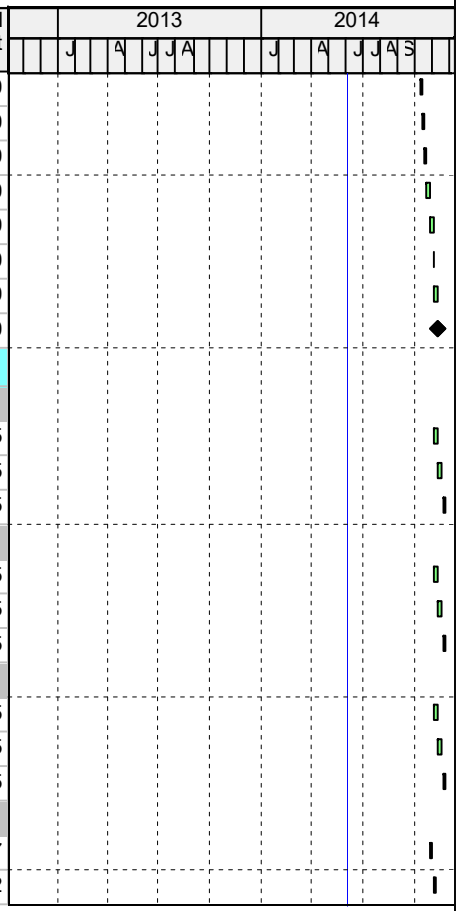



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Working Schedule - 7-11-14 Update** | | | | | | |
| I-1500 | Owner release revised LV design - Tower (ASIs 5, 13, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-1550 | Owner release revised LV design - Podium (ASIs 5, 1 | 200 | 0 | 23-May-13 A | 28-Apr-14 A | |
| I-1900 | Owner issue design revisions (ASIs 4, 9, 19, 34) | 215 | 0 | 23-May-13 A | 24-Mar-14 A | |
| I-2500 | Owner issue LL1 electrical revisions (ASIs 7, 9r2, 14, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-3400 | Owner provide Level 2 ceiling heights | 180 | 0 | 24-Jun-13 A | 24-Mar-14 A | |
| I-3700 | Owner resolve wall condition between stair and Eleva | 200 | 0 | 27-Jun-13 A | 16-Jun-14 A | |
| MM-1000 | MM - Temporary Power Available | 0 | 0 | 08-Jul-13 A | | |
| I-2100 | Owner revise roof steel design (Submittals 365, 370, | 200 | 0 | 09-Jul-13 A | 07-Apr-14 A | |
| I-2200 | Owner resolve elevator steel issue (RFI 112, RFI 112. | 200 | 0 | 09-Jul-13 A | 03-Mar-14 A | |
| I-2400 | Owner provide Tower light fixture selections (ASI 36) | 185 | 0 | 18-Jul-13 A | 08-Apr-14 A | |
| I-2900 | Owner revise Food Service and Kitchen (ASIs 11, 12, | 140 | 0 | 08-Aug-13 A | 27-Feb-14 A | |
| I-1400 | Owner develop envelope redesign | 70 | 0 | 27-Aug-13 A | 12-Dec-13 A | |
| I-3600 | Owner closeout glass/glazing allowance | 160 | 0 | 04-Sep-13 A | 30-Apr-14 A | |
| I-1200 | Owner release revised Concierge Lounge design (AS | 160 | 0 | 06-Sep-13 A | 08-Apr-14 A | |
| I-2800 | Owner revise interior public space design (ASIs 16, 1 | 130 | 0 | 25-Sep-13 A | 09-Apr-14 A | |
| I-2000 | Owner approve door frames (Submittals 258, 454, 48 | 85 | 0 | 27-Sep-13 A | 23-Jan-14 A | |
| I-3100 | Owner revise ballroom ceiling design (ASIs 18, 25) | 100 | 0 | 17-Oct-13 A | 25-Feb-14 A | |
| I-1600 | Owner provide directive for south & east corridor encl | 110 | 0 | 28-Oct-13 A | 18-Apr-14 A | |
| I-2300 | Owner resolve fire smoke dampers issue (RFI 233) | 115 | 0 | 30-Oct-13 A | 11-Apr-14 A | |
| I-2600 | Owner resolve L2 slab coordination issue | 4 | 0 | 13-Nov-13 A | 16-Nov-13 A | |
| I-2700 | Owner revise tower guest rooms design (ASIs 23, 29) | 58 | 0 | 04-Dec-13 A | 26-Feb-14 A | |
| I-1700 | Owner provide design for dry site utilities (ASIs 20, 20 | 66 | 0 | 09-Dec-13 A | 13-Mar-14 A | |
| I-1402 | Begin exterior panel production | 41 | 0 | 13-Dec-13 A | 12-Feb-14 A | |
| I-1300 | Owner issue "Hold" directive (email) | 0 | 0 | | 19-Dec-13 A | |
| I-1100 | Owner release revised L17 design (ASI 23, 29R1) | 74 | 0 | 20-Dec-13 A | 08-Apr-14 A | |
| I-1302 | Owner issue ASI 30 (Prep Kitchen Revisions) | 47 | 0 | 20-Dec-13 A | 27-Feb-14 A | |

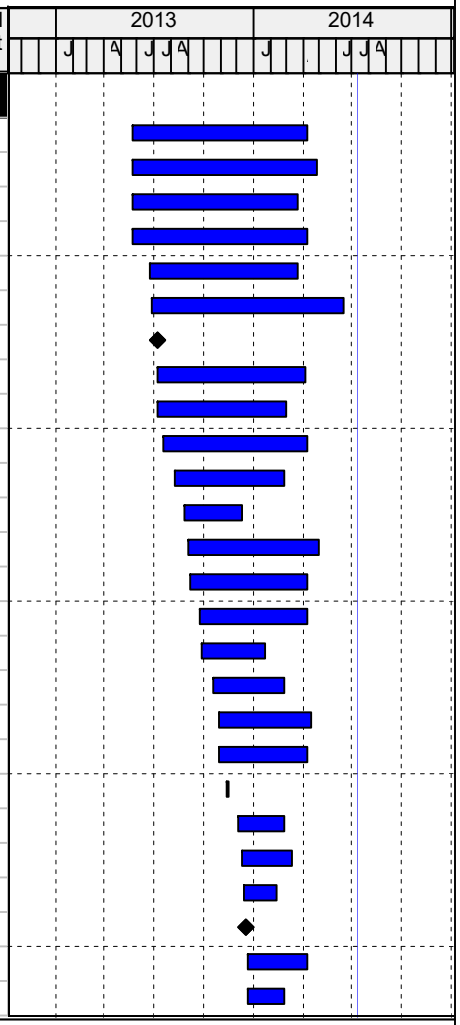


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| High Rise Hotel Sample Project | All Activities | Schedule Status Date 12-Jul-14 |
|---|---|---|

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1404 | City of Bellevue Approval | 90 | 2 | 23-Dec-13 A | 15-Jul-14 | 59 |
| I-3000 | Owner revise bar area (change to straight bar, IDRFI-( | 71 | 0 | 22-Jan-14 A | 27-May-14 A | |
| I-1306 | Prep Kitchen - Additional plumbing (ASI 30) | 4 | 2 | 17-Feb-14 A | 16-Jul-14 | 23 |
| I-2202 | Fabricate revised elevator steel | 60 | 0 | 04-Mar-14 A | 07-May-14 A | |
| I-2704 | Framing "Go Back" work for ASIs 23, 29 - L4 | 1 | 0 | 05-Mar-14 A | 12-Mar-14 A | |
| I-3900 | RFI 471, Resolve Ballroom parapet height issue | 1 | 0 | 08-Mar-14 A | 07-May-14 A | |
| I-1702 | Owner provide directive to proceed | 26 | 0 | 14-Mar-14 A | 01-May-14 A | |
| I-3300 | Owner provide Guest Room plumbing fixture selectio | 1 | 0 | 20-Mar-14 A | 20-Mar-14 A | |
| I-1902 | Procure revised structural steel | 15 | 0 | 25-Mar-14 A | 14-Apr-14 A | |
| I-4000 | Owner complete design of east stitched enclosure (fo | 1 | 0 | 01-Apr-14 A | 14-May-14 A | |
| I-2102 | Fabricate revised roof steel | 20 | 0 | 08-Apr-14 A | 15-May-14 A | |
| I-3200 | Owner provide light fixture selections for podium level | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| I-3800 | Resolve Heat Pump Electrical Overcurrent Issue | 20 | 0 | 23-Apr-14 A | 18-Jun-14 A | |
| L10-8221 | HVAC Risers Duct Insulation | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L11-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| I-2304 | Framing "Go Back" work at L3 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2306 | Framing "Go Back" work at L4 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2308 | Framing "Go Back" work at L5 for RFI 233 | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2706 | Framing "Go Back" work for ASIs 23, 29 - L5 | 1 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2708 | Framing "Go Back" work for ASIs 23, 29 - L6 | 1 | 0 | 29-Apr-14 A | 09-May-14 A | |
| I-2702 | Framing "Go Back" work for ASIs 23, 29 - L3 | 1 | 0 | 01-May-14 A | 01-May-14 A | |
| I-1706 | PSE scheduling delay | 10 | 0 | 01-May-14 A | 20-May-14 A | |
| I-3602 | Complete shop drawings & fab/deliver storefront fram | 40 | 0 | 01-May-14 A | 14-Jun-14 A | |
| L04-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| I-1802 | Rework framing for door hold-opens - LL4 | 1 | 0 | 07-May-14 A | 08-May-14 A | |
| L04-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-May-14 A | 12-May-14 A | |

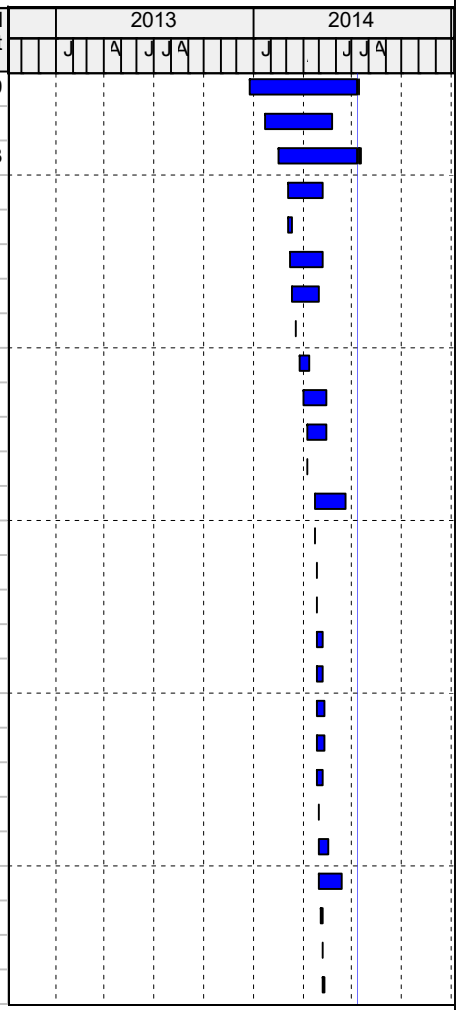



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1800 | Owner issue directive to proceed with door hold-open | 1 | 0 | 08-May-14 A | 08-May-14 A | |
| I-1804 | Rework framing for door hold-opens - LL3 | 1 | 0 | 08-May-14 A | 09-May-14 A | |
| I-2312 | Framing "Go Back" work at L7 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-2314 | Framing "Go Back" work at L8 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-3902 | Install Ballroom parapet extension | 5 | 0 | 08-May-14 A | 13-May-14 A | |
| I-1806 | Rework framing for door hold-opens - LL2 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-1808 | Rework framing for door hold-opens - LL1 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-2310 | Framing "Go Back" work at L6 for RFI 233 | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| I-2710 | Framing "Go Back" work for ASIs 23, 29 - L7 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| L05-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L06-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L05-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| LL2E-8110 | LL2 - Electtrical, Fire pumps/equipment final connecti | 5 | 4 | 12-May-14 A | 01-Aug-14 | 34 |
| PH-8704 | PH - Install Machine Support Steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| PH-8710 | Install elevator rail support steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| L03-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L03-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 13-May-14 A | 14-May-14 A | |
| I-4002 | East Stitched - Install framing and windows | 9 | 0 | 19-May-14 A | 09-Jun-14 A | |
| L10-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L11-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L12-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| RF-4038 | AR - Concrete pads and curbs | 5 | 0 | 21-May-14 A | 04-Jun-14 A | |
| L10-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L11-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L12-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L14-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |

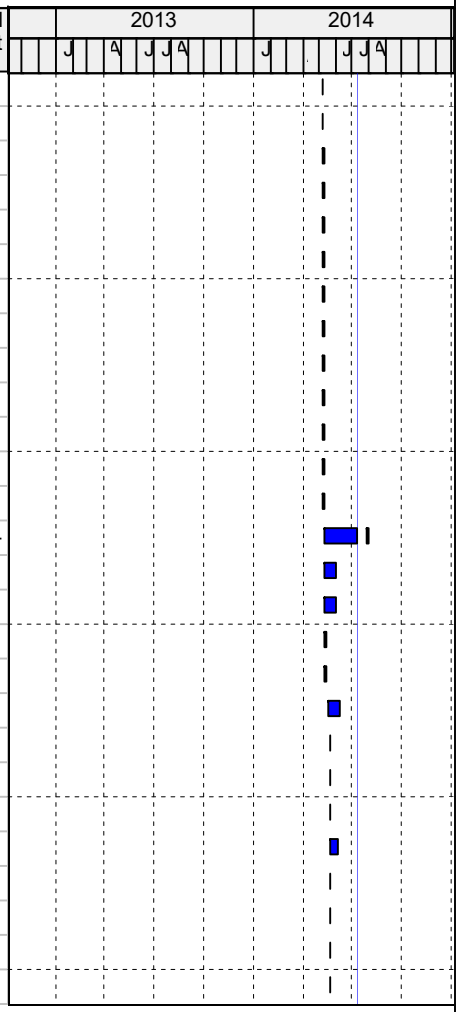



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 27-May-14 A | |
| L11-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 07-Jun-14 A | |
| L12-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 27-May-14 A | 06-Jun-14 A | |
| I-3002 | City of Bellevue approve bar design changes. | 5 | 2 | 28-May-14 A | 15-Jul-14 | 26 |
| L16-8221 | HVAC Risers Duct Insulation | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| PH-8712 | PH - Complete Framing and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| PH-8714 | Stage PH/L18 roofing materials | 2 | 0 | 30-May-14 A | 30-May-14 A | |
| L08-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L08-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 02-Jun-14 A | 20-Jun-14 A | |
| PH-8704I | Correct support steel embeds | 2 | 0 | 02-Jun-14 A | 11-Jun-14 A | |
| L14-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 03-Jun-14 A | 04-Jun-14 A | |
| L17-8221 | HVAC Risers Duct Insulation | 1 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| PC-4010 | PC - Fireproof Entry Roof Steel | 5 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| I-4100 | Owner resolve trap primers issue (RFI 560) | 5 | 0 | 03-Jun-14 A | 20-Jun-14 A | |
| RF-6028 | Tower Roof - Structural Steel | 5 | 0 | 04-Jun-14 A | 17-Jun-14 A | |
| L14-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L1B-6005 | Head of Wall Fire Caulk at CMU (including East Servi | 2 | 1 | 05-Jun-14 A | 14-Jul-14 | 113 |
| L14-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L15-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L16-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |

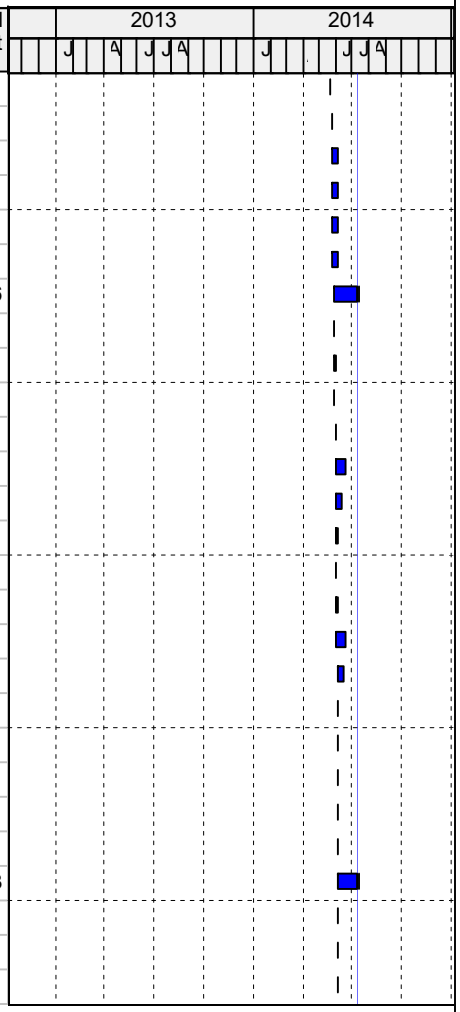



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 11-Jun-14 A | 12-Jun-14 A | |
| I-3702 | Complete wall framing at Stair/Elevator 5 (LL4) | 2 | 0 | 18-Jun-14 A | 20-Jun-14 A | |
| I-3720 | Fireproof added steel between Stair 1 and Elevator 5 | 5 | 2 | 18-Jun-14 A | 15-Jul-14 | 17 |
| I-3722 | Complete GWB between Stair 1 and Elevator 5 shaft | 10 | 2 | 18-Jun-14 A | 17-Jul-14 | 17 |
| LL1-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 7 | 19-Jun-14 A | 22-Jul-14 | 26 |
| TC-5912 | Tower Crane pour-backs (LL4 to L3) | 4 | 0 | 19-Jun-14 A | 26-Jun-14 A | |
| LL1-Z2-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 4 | 19-Jun-14 A | 17-Jul-14 | 27 |
| LL4-6005 | LL4 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 20-Jun-14 A | |
| LL3-6005 | LL3 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 20-Jun-14 A | |
| L03-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 21-Jun-14 A | 21-Jun-14 A | |
| L06-6040 | Test Heat Pumps - L3, L4, L5 and L6 | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L03-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| L17-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL2-6005 | LL2 - Seismic Head Of Wall Fire Caulk at CMU | 5 | 2 | 24-Jun-14 A | 15-Jul-14 | 38 |
| I-3704 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL1-6005 | Head of Wall Fire Caulk at CMU | 2 | 1 | 24-Jun-14 A | 14-Jul-14 | 25 |
| LL1-Z2-6005 | Head of Wall Fire Caulk at CMU | 2 | 1 | 24-Jun-14 A | 14-Jul-14 | 112 |
| LL1-Z3-6005 | Head of Wall Fire Caulk at CMU (At All Areas North of | 2 | 1 | 24-Jun-14 A | 15-Jul-14 | 112 |
| L1L-6005 | Head of Wall Fire Caulk at CMU (including back of ho | 2 | 1 | 24-Jun-14 A | 14-Jul-14 | 9 |
| L1K-6005 | Head of Wall Fire Caulk at CMU (including public rest | 2 | 1 | 24-Jun-14 A | 14-Jul-14 | 113 |
| L03-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L04-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| I-3710 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 1 | 25-Jun-14 A | 14-Jul-14 | 41 |
| I-3712 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 25-Jun-14 A | 08-Jul-14 A | |
| L1K-6018a | Install Kitchen hoods and grease ducts (OFCI) | 10 | 8 | 25-Jun-14 A | 05-Aug-14 | 23 |
| L03-8604 | L3 Pool - Plumbing R/I | 5 | 4 | 25-Jun-14 A | 23-Jul-14 | 67 |

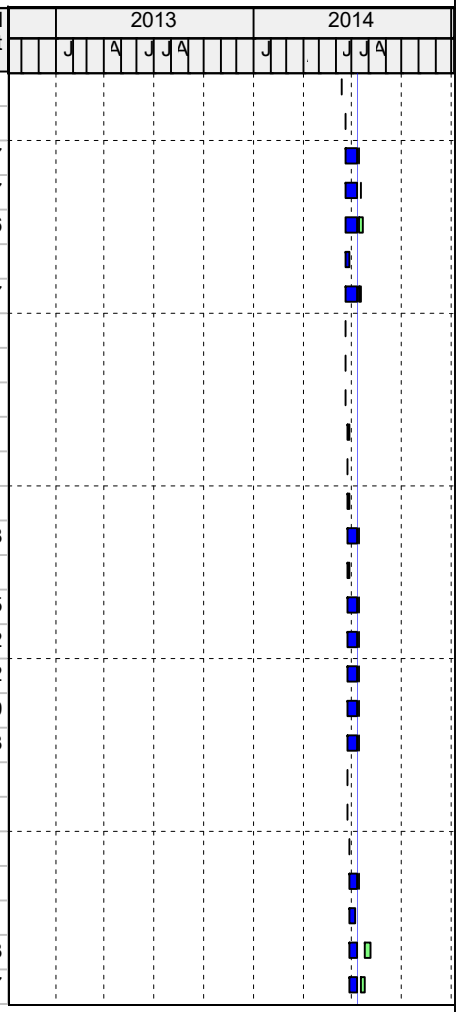



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 26-Jun-14 A | 03-Jul-14 A | |
| L09-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 26-Jun-14 A | 26-Jun-14 A | |
| I-3706 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 26-Jun-14 A | 10-Jul-14 A | |
| L03-8600 | L3 Pool - Framing & HM frames | 5 | 4 | 26-Jun-14 A | 17-Jul-14 | 66 |
| L05-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L08-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 27-Jun-14 A | 14-Jul-14 | 12 |
| L04-7018 | Electrical Rough-In | 1 | 1 | 27-Jun-14 A | 22-Jul-14 | 68 |
| L04-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 27-Jun-14 A | 23-Jul-14 | 68 |
| L03-7020 | HVAC Rough-In | 1 | 1 | 29-Jun-14 A | 15-Jul-14 | 74 |
| L03-7018 | Electrical Rough-In | 1 | 1 | 01-Jul-14 A | 14-Jul-14 | 74 |
| L03-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 01-Jul-14 A | 15-Jul-14 | 74 |
| L10-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7102 | Install Vertical Heat Pump | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L03-7116 | Frame Walls | 1 | 1 | 02-Jul-14 A | 14-Jul-14 | 78 |
| L03-7118 | Install HM Door Frame | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L04-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L05-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L07-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L08-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L09-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L10-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L12-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |

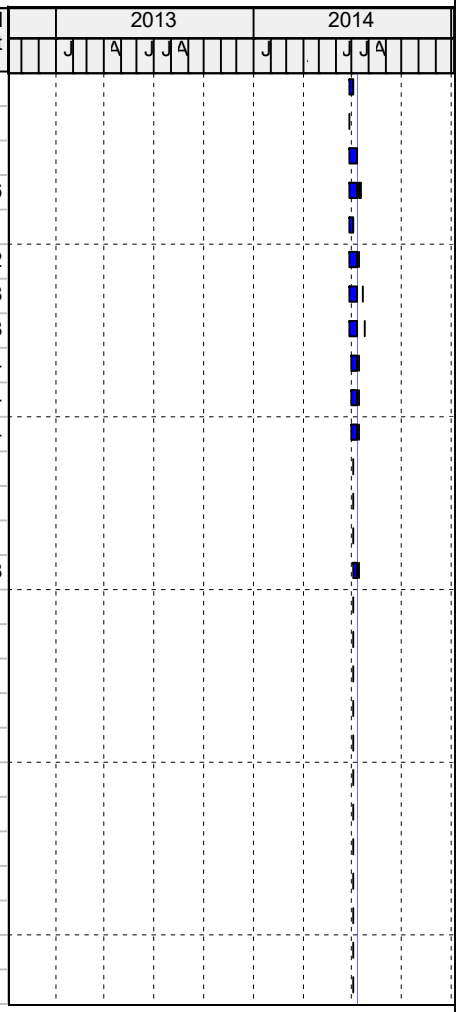



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-3708 | Complete wall framing at Stair/Elevator 5 (LL3) | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L11-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 03-Jul-14 A | 07-Jul-14 A | |
| L04-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L05-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L06-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L07-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L08-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L17-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 1 | 07-Jul-14 A | 14-Jul-14 | 38 |
| L10-6040 | Test Heat Pumps - L7, L8, L9 and L10 | 3 | 0 | 07-Jul-14 A | 09-Jul-14 A | |
| L10-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L03-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L04-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L05-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L06-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L07-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L08-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |

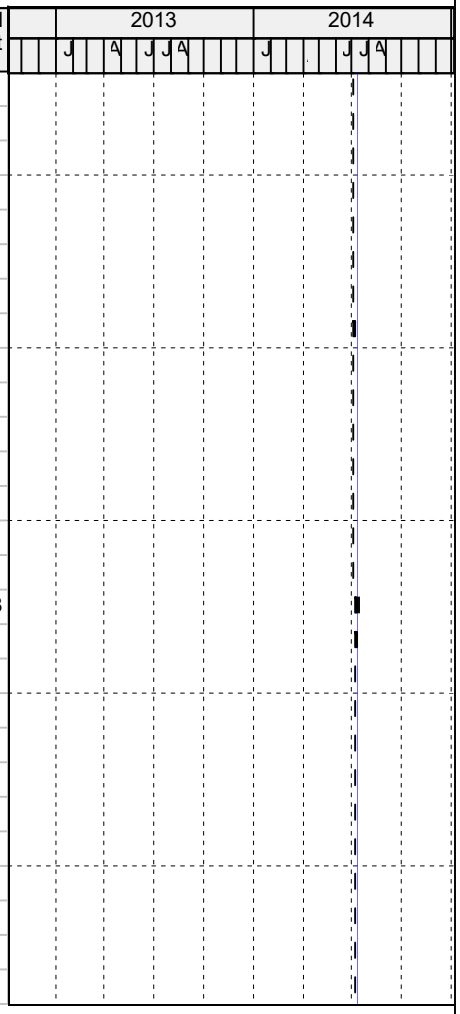



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L10-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L12-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L14-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L11-6036 | Framing Around Heat Pump & Soffit | 3 | 1 | 08-Jul-14 A | 16-Jul-14 | 21 |
| L03-8602 | L3 Pool - Fire Sprinkler R/I | 5 | 3 | 08-Jul-14 A | 22-Jul-14 | 68 |
| L03-7016 | Install HM door frame | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L11-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L16-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 09-Jul-14 A | |
| L04-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |

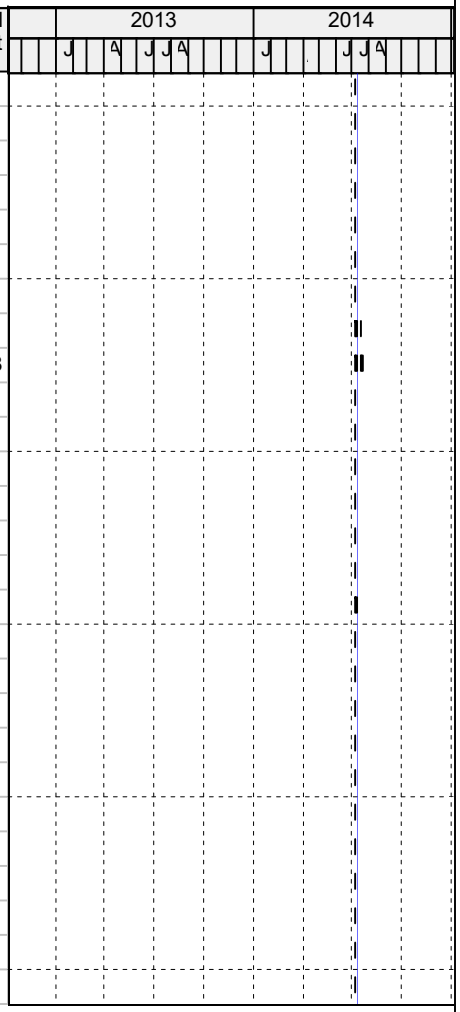



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L12-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| MP-FAB1 | Fabricate and Deliver Bronze Gold Horizontal Panels | 30 | 11 | 09-Jul-14 A | 28-Jul-14 | 50 |
| L04-7116 | Frame Walls | 1 | 1 | 09-Jul-14 A | 14-Jul-14 | 78 |
| L05-7116 | Frame Walls | 1 | 1 | 09-Jul-14 A | 14-Jul-14 | 78 |
| L06-7116 | Frame Walls | 1 | 1 | 09-Jul-14 A | 14-Jul-14 | 78 |
| L16-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| MP-FAB2 | Fabricate and Deliver Silver Vertical Panels | 45 | 11 | 10-Jul-14 A | 28-Jul-14 | 65 |
| L07-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 8 |
| LL2-2046 | LL2 - Generator Room build-out | 20 | 20 | 14-Jul-14 | 08-Aug-14 | 76 |
| LL1-Z2-6018a | Complete Mech RI at tower crane opening (LL1) | 4 | 4 | 14-Jul-14 | 17-Jul-14 | 34 |
| LL2-2052 | LL2 - Install fuel piping and exhaust duct to Generatc | 5 | 5 | 14-Jul-14* | 18-Jul-14 | 50 |
| L04-6005 | CMU Fire Caulk/Clips | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 4 |
| I-4102 | Install added trap primers - LL2 | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 43 |
| I-4104 | Install added trap primers - LL1 | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 30 |

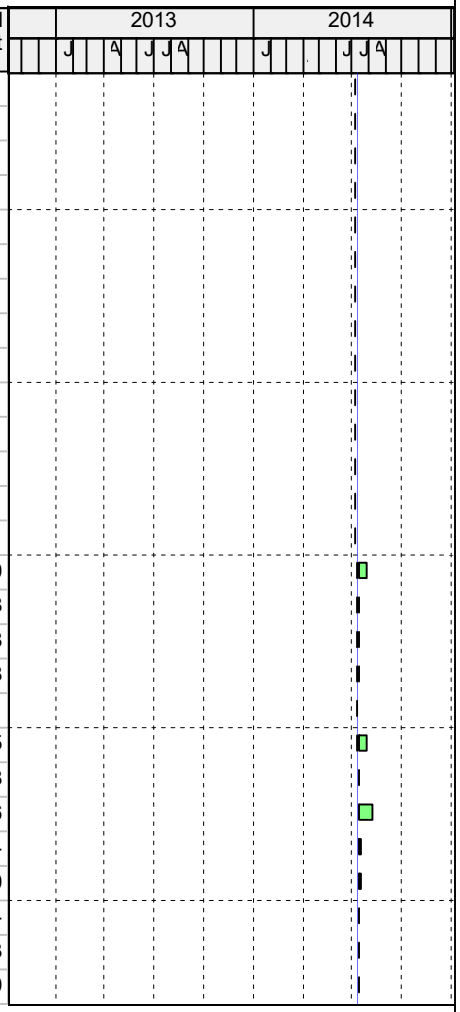



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-4106 | Install added trap primers - L1 | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 39 |
| I-4108 | Install added trap primers - L2 | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 42 |
| I-4110 | Install added trap primers - L3 | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 0 |
| I-4112 | Install added trap primers - Roof PH | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 45 |
| L08-6223 | Frame Corridor Ceilings | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 11 |
| L09-6223 | Frame corridor ceilings | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 15 |
| SW-2006a | Complete Dry Utilities (Phase 2) | 5 | 5 | 14-Jul-14* | 18-Jul-14 | 86 |
| L04-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 68 |
| L04-7004 | HVAC Firestop & Inspect (1) | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 69 |
| L05-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 67 |
| L05-7004 | HVAC Firestop & Inspect (1) | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 68 |
| L06-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 67 |
| L06-7004 | HVAC Firestop & Inspect (1) | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 68 |
| L07-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 67 |
| L07-7004 | HVAC Firestop & Inspect (1) | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 68 |
| L08-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 67 |
| L08-7004 | HVAC Firestop & Inspect (1) | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 68 |
| L09-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 67 |
| L09-7004 | HVAC Firestop & Inspect (1) | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 68 |
| L10-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 67 |
| L10-7004 | HVAC Firestop & Inspect (1) | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 68 |
| L11-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 67 |
| L12-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 67 |
| L12-7004 | HVAC Firestop & Inspect (1) | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 68 |
| L14-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 67 |
| L14-7004 | HVAC Firestop & Inspect (1) | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 68 |
| L15-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 63 |

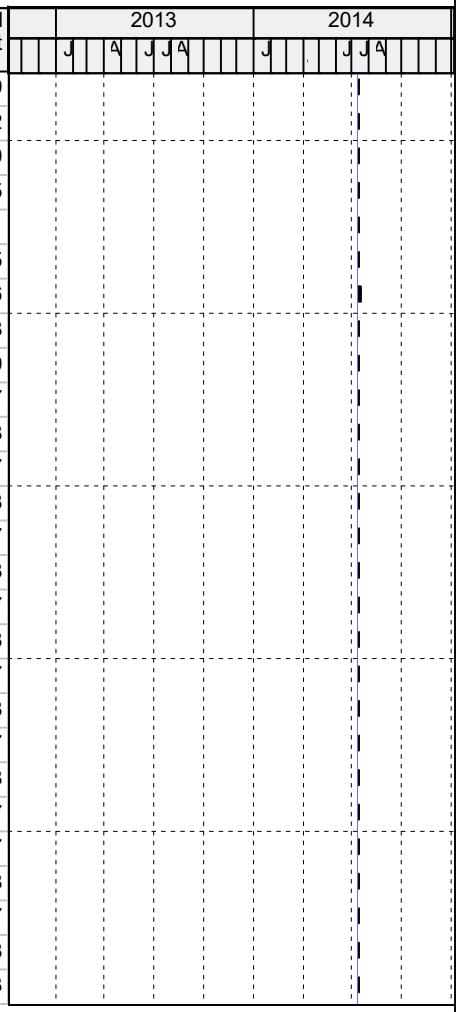



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7118 | Install HM Door Frame | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 81 |
| L05-7118 | Install HM Door Frame | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 81 |
| L06-7118 | Install HM Door Frame | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 81 |
| L07-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 75 |
| L07-7110 | HVAC Firestop & Inspect (2) | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 115 |
| L08-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 75 |
| L08-7110 | HVAC Firestop & Inspect (2) | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 115 |
| L09-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 75 |
| L09-7110 | HVAC Firestop & Inspect (2) | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 115 |
| L10-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 73 |
| L10-7106 | HVAC Firestop & Inspect (1) | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 115 |
| L11-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 73 |
| L11-7106 | HVAC Firestop & Inspect (1) | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 115 |
| L12-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 73 |
| L12-7106 | HVAC Firestop & Inspect (1) | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 115 |
| L14-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 73 |
| L14-7106 | HVAC Firestop & Inspect (1) | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 115 |
| L15-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 69 |
| L15-7102 | Install Vertical Heat Pump | 1 | 1 | 14-Jul-14 | 14-Jul-14 | 72 |
| I-1304 | Prep Kitchen - Additional framing (ASI 30) | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 31 |
| I-2302 | Framing "Go Back" work at LL1 for RFI 233 | 3 | 3 | 15-Jul-14 | 17-Jul-14 | 27 |
| LL2-2048 | LL2 - Set Laundry Room equipment (BY OTHERS) | 2 | 2 | 15-Jul-14* | 16-Jul-14 | 103 |
| LL1-6014la | L1 bar redesign - rework plumbing at ceilings | 1 | 1 | 15-Jul-14 | 15-Jul-14 | 26 |
| L1B-6026 | Install operable partition track | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 21 |
| L10-6223 | Frame Corridor Ceilings | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 18 |
| L03-7120 | Electrical Rough-In | 1 | 1 | 15-Jul-14 | 15-Jul-14 | 78 |
| L04-7120 | Electrical Rough-In | 1 | 1 | 15-Jul-14 | 15-Jul-14 | 78 |

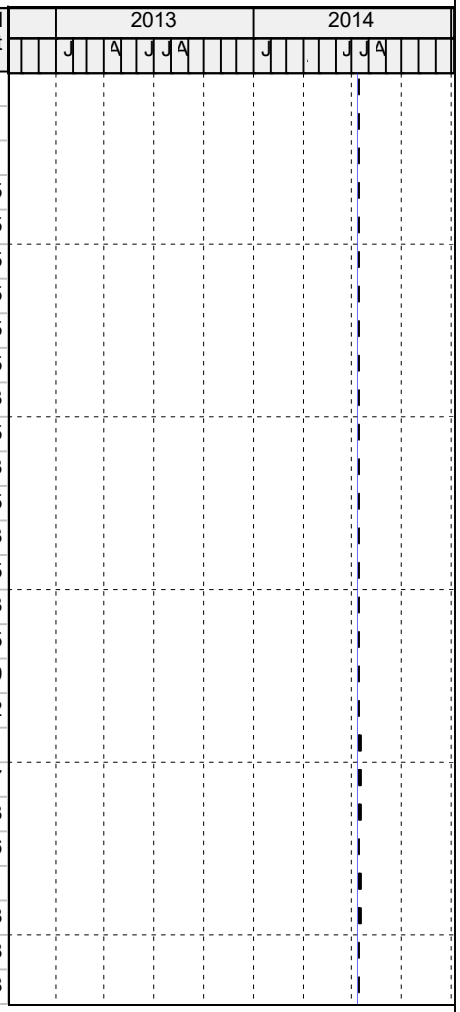



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7120 | Electrical Rough-In | 1 | 1 | 15-Jul-14 | 15-Jul-14 | 78 |
| L06-7120 | Electrical Rough-In | 1 | 1 | 15-Jul-14 | 15-Jul-14 | 78 |
| L07-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 75 |
| L07-7114 | HVAC Firestop & Inspect (3) | 1 | 1 | 15-Jul-14 | 15-Jul-14 | 114 |
| L08-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 75 |
| L08-7114 | HVAC Firestop & Inspect (3) | 1 | 1 | 15-Jul-14 | 15-Jul-14 | 114 |
| L09-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 75 |
| L09-7114 | HVAC Firestop & Inspect (3) | 1 | 1 | 15-Jul-14 | 15-Jul-14 | 114 |
| L03-7142 | Install Laundry Chute (All Levels) | 9 | 9 | 15-Jul-14* | 25-Jul-14 | 73 |
| L11-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 21 |
| L12-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 25 |
| L14-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 29 |
| L15-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 112 |
| L14-6040 | Test Heat Pumps - L11, L12 and L14 | 3 | 3 | 16-Jul-14 | 18-Jul-14 | 21 |
| L14-6036 | Framing Around Heat Pump & Soffit | 3 | 3 | 16-Jul-14 | 18-Jul-14 | 27 |
| L12-6036 | Framing Around Heat Pump & Soffit | 3 | 3 | 16-Jul-14 | 18-Jul-14 | 24 |
| L15-6036 | Framing Around Heat Pump & Soffit | 3 | 3 | 16-Jul-14 | 18-Jul-14 | 31 |
| LL1-6014lb | L1 bar redesign - rework ceiling framing | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 29 |
| L05-6005 | CMU Fire Caulk/Clips | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 4 |
| L11-6223 | Frame Corridor Ceilings | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 21 |
| L03-7026 | Inspections for GWB Cover | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 74 |
| L03-7122 | HVAC Rough-In | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 78 |
| L03-7124 | Fire Sprinkler Rough-In | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 78 |
| L04-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 68 |
| L04-7008 | HVAC Firestop & Inspect (2) | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 68 |
| L05-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 67 |
| L05-7008 | HVAC Firestop & Inspect (2) | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 67 |

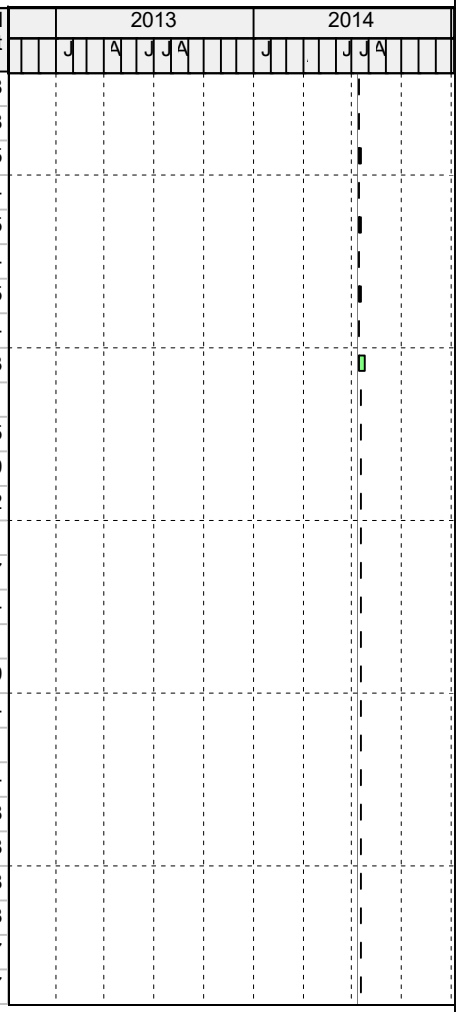



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 67 |
| L06-7008 | HVAC Firestop & Inspect (2) | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 67 |
| L07-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 67 |
| L07-7008 | HVAC Firestop & Inspect (2) | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 67 |
| L08-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 67 |
| L08-7008 | HVAC Firestop & Inspect (2) | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 67 |
| L09-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 67 |
| L09-7008 | HVAC Firestop & Inspect (2) | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 67 |
| L10-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 67 |
| L10-7008 | HVAC Firestop & Inspect (2) | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 67 |
| L11-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 67 |
| L11-7008 | HVAC Firestop & Inspect (2) | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 67 |
| L12-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 67 |
| L12-7008 | HVAC Firestop & Inspect (2) | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 67 |
| L14-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 67 |
| L14-7008 | HVAC Firestop & Inspect (2) | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 67 |
| L15-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 65 |
| L15-7004 | HVAC Firestop & Inspect (1) | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 66 |
| L16-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 65 |
| L16-7004 | HVAC Firestop & Inspect (1) | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 66 |
| L17-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 63 |
| L04-7122 | HVAC Rough-In | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 78 |
| L04-7124 | Fire Sprinkler Rough-In | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 78 |
| L05-7122 | HVAC Rough-In | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 78 |
| L05-7124 | Fire Sprinkler Rough-In | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 78 |
| L06-7122 | HVAC Rough-In | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 78 |
| L06-7124 | Fire Sprinkler Rough-In | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 78 |

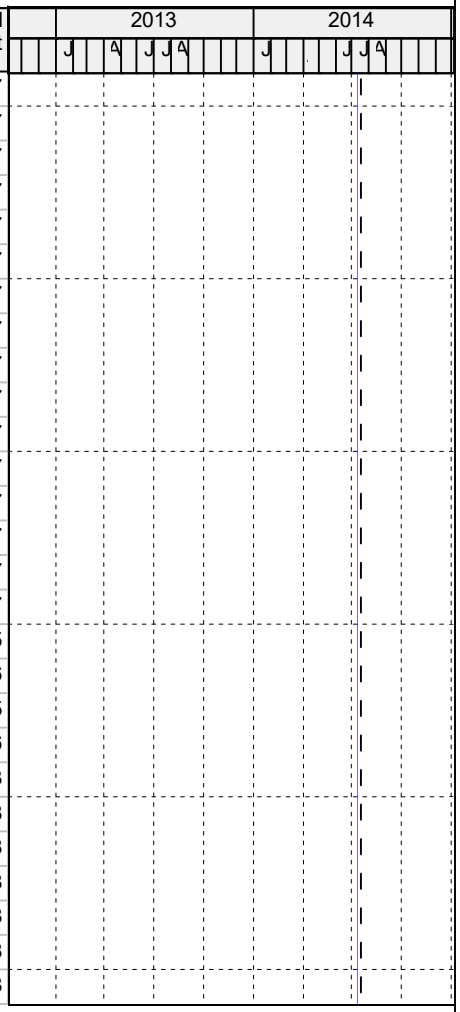



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 73 |
| L10-7110 | HVAC Firestop & Inspect (2) | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 113 |
| L11-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 73 |
| L11-7110 | HVAC Firestop & Inspect (2) | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 113 |
| L12-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 73 |
| L12-7110 | HVAC Firestop & Inspect (2) | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 113 |
| L14-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 73 |
| L14-7110 | HVAC Firestop & Inspect (2) | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 113 |
| L15-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 71 |
| L15-7106 | HVAC Firestop & Inspect (1) | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 113 |
| L16-7102 | Install Vertical Heat Pump | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 70 |
| L17-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 69 |
| L17-7102 | Install Vertical Heat Pump | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 70 |
| L11-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 21 |
| LL2-2050 | LL2 - Laundry Room equipment final connections (MI | 10 | 10 | 17-Jul-14 | 30-Jul-14 | 103 |
| L03-7028 | GWB Hang/Tape/Finish | 5 | 5 | 17-Jul-14 | 23-Jul-14 | 74 |
| L03-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 78 |
| L04-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 68 |
| L04-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 69 |
| L05-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 67 |
| L05-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 68 |
| L06-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 67 |
| L06-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 68 |
| L07-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 67 |
| L07-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 68 |
| L08-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 67 |
| L08-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 68 |

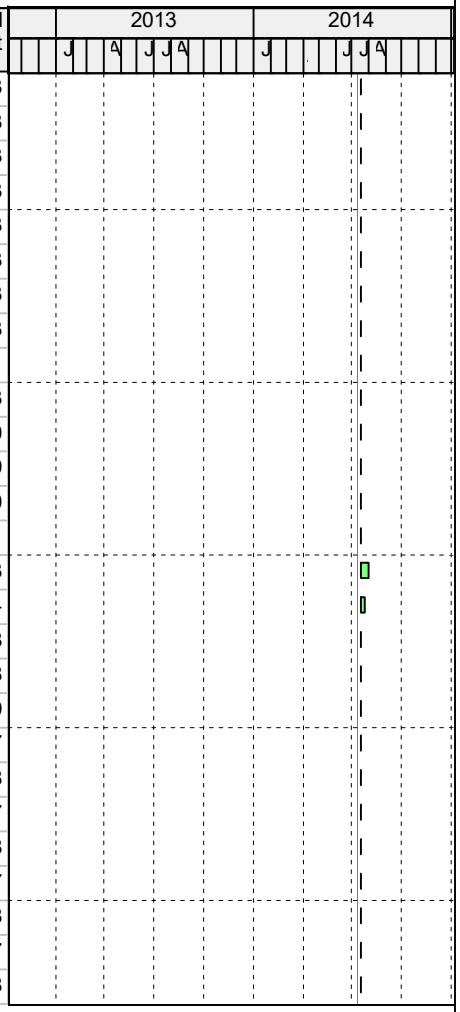



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 67 |
| L09-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 68 |
| L10-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 67 |
| L10-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 68 |
| L11-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 67 |
| L11-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 68 |
| L12-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 67 |
| L12-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 68 |
| L14-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 67 |
| L14-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 68 |
| L04-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 78 |
| L05-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 78 |
| L06-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 78 |
| L07-7116 | Frame Walls | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 75 |
| L07-7118 | Install HM Door Frame | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 78 |
| L08-7116 | Frame Walls | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 75 |
| L08-7118 | Install HM Door Frame | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 78 |
| L09-7116 | Frame Walls | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 75 |
| L09-7118 | Install HM Door Frame | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 78 |
| L10-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 73 |
| L10-7114 | HVAC Firestop & Inspect (3) | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 112 |
| L11-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 73 |
| L11-7114 | HVAC Firestop & Inspect (3) | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 112 |
| L12-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 73 |
| L12-7114 | HVAC Firestop & Inspect (3) | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 112 |
| L14-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 73 |
| L14-7114 | HVAC Firestop & Inspect (3) | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 112 |

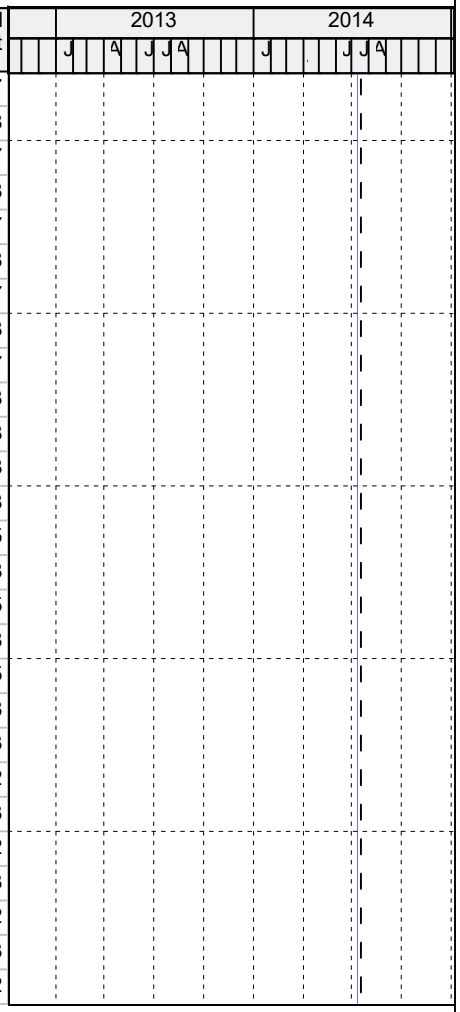



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 70 |
| L16-7106 | HVAC Firestop & Inspect (1) | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 112 |
| L12-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 18-Jul-14 | 18-Jul-14 | 24 |
| L03-8606 | L3 Pool - HVAC R/I | 5 | 5 | 18-Jul-14 | 24-Jul-14 | 66 |
| L03-8608 | L3 Pool - Electrical R/I | 5 | 5 | 18-Jul-14 | 24-Jul-14 | 66 |
| L03-8610 | L3 Pool - Fire Alarm / Elec Specialties R/I | 5 | 5 | 18-Jul-14 | 24-Jul-14 | 66 |
| L06-6005 | CMU Fire Caulk/Clips | 2 | 2 | 18-Jul-14 | 21-Jul-14 | 4 |
| L03-7128 | Inspections for GWB Cover | 1 | 1 | 18-Jul-14 | 18-Jul-14 | 78 |
| L15-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 18-Jul-14 | 21-Jul-14 | 65 |
| L15-7008 | HVAC Firestop & Inspect (2) | 1 | 1 | 18-Jul-14 | 18-Jul-14 | 65 |
| L16-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 18-Jul-14 | 21-Jul-14 | 65 |
| L16-7008 | HVAC Firestop & Inspect (2) | 1 | 1 | 18-Jul-14 | 18-Jul-14 | 65 |
| L17-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 18-Jul-14 | 21-Jul-14 | 63 |
| L17-7004 | HVAC Firestop & Inspect (1) | 1 | 1 | 18-Jul-14 | 18-Jul-14 | 64 |
| L04-7128 | Inspections for GWB Cover | 1 | 1 | 18-Jul-14 | 18-Jul-14 | 78 |
| L05-7128 | Inspections for GWB Cover | 1 | 1 | 18-Jul-14 | 18-Jul-14 | 78 |
| L06-7128 | Inspections for GWB Cover | 1 | 1 | 18-Jul-14 | 18-Jul-14 | 78 |
| L07-7120 | Electrical Rough-In | 1 | 1 | 18-Jul-14 | 18-Jul-14 | 75 |
| L08-7120 | Electrical Rough-In | 1 | 1 | 18-Jul-14 | 18-Jul-14 | 75 |
| L09-7120 | Electrical Rough-In | 1 | 1 | 18-Jul-14 | 18-Jul-14 | 75 |
| L15-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 18-Jul-14 | 21-Jul-14 | 71 |
| L15-7110 | HVAC Firestop & Inspect (2) | 1 | 1 | 18-Jul-14 | 18-Jul-14 | 111 |
| L17-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 18-Jul-14 | 21-Jul-14 | 69 |
| L17-7106 | HVAC Firestop & Inspect (1) | 1 | 1 | 18-Jul-14 | 18-Jul-14 | 111 |
| L14-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 27 |
| L15-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 31 |
| L03-7130 | GWB Hang/Tape/Finish | 5 | 5 | 21-Jul-14 | 25-Jul-14 | 78 |

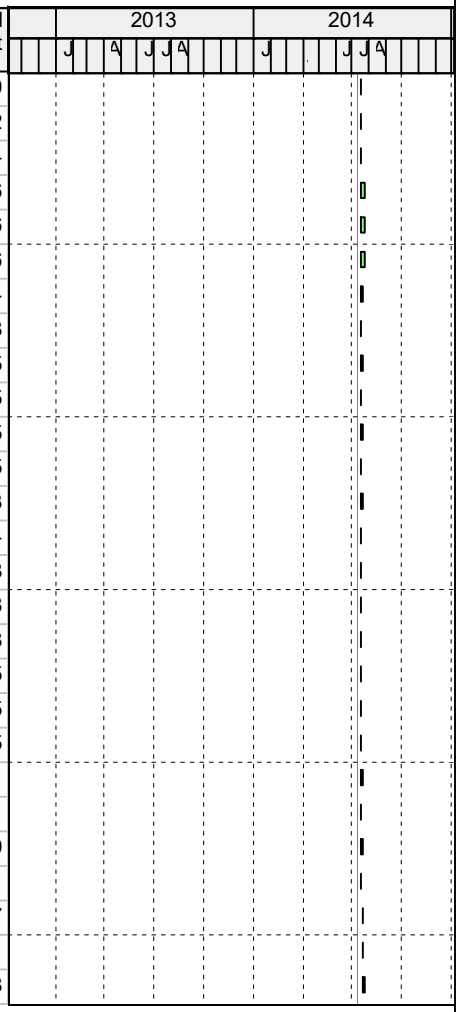



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 68 |
| L04-7016 | Install HM door frame | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 70 |
| L05-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 67 |
| L05-7016 | Install HM door frame | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 70 |
| L06-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 67 |
| L06-7016 | Install HM door frame | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 70 |
| L07-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 67 |
| L07-7016 | Install HM door frame | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 70 |
| L08-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 67 |
| L08-7016 | Install HM door frame | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 70 |
| L09-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 67 |
| L09-7016 | Install HM door frame | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 70 |
| L10-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 67 |
| L10-7016 | Install HM door frame | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 70 |
| L11-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 67 |
| L11-7016 | Install HM door frame | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 70 |
| L12-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 67 |
| L12-7016 | Install HM door frame | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 70 |
| L14-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 67 |
| L14-7016 | Install HM door frame | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 70 |
| L15-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 21-Jul-14 | 22-Jul-14 | 65 |
| L15-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 66 |
| L16-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 21-Jul-14 | 22-Jul-14 | 65 |
| L16-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 66 |
| L04-7130 | GWB Hang/Tape/Finish | 5 | 5 | 21-Jul-14 | 25-Jul-14 | 78 |
| L05-7130 | GWB Hang/Tape/Finish | 5 | 5 | 21-Jul-14 | 25-Jul-14 | 78 |
| L06-7130 | GWB Hang/Tape/Finish | 5 | 5 | 21-Jul-14 | 25-Jul-14 | 78 |

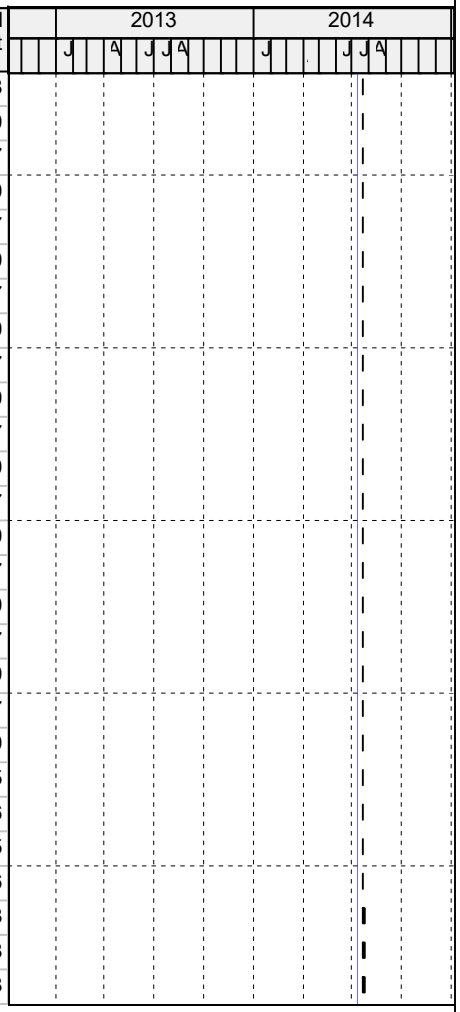



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7122 | HVAC Rough-In | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 75 |
| L07-7124 | Fire Sprinkler Rough-In | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 75 |
| L08-7122 | HVAC Rough-In | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 75 |
| L08-7124 | Fire Sprinkler Rough-In | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 75 |
| L09-7122 | HVAC Rough-In | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 75 |
| L09-7124 | Fire Sprinkler Rough-In | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 75 |
| L10-7116 | Frame Walls | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 73 |
| L10-7118 | Install HM Door Frame | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 76 |
| L11-7116 | Frame Walls | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 73 |
| L11-7118 | Install HM Door Frame | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 76 |
| L12-7116 | Frame Walls | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 73 |
| L12-7118 | Install HM Door Frame | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 76 |
| L14-7116 | Frame Walls | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 73 |
| L14-7118 | Install HM Door Frame | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 76 |
| L15-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 21-Jul-14 | 22-Jul-14 | 71 |
| L15-7114 | HVAC Firestop & Inspect (3) | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 110 |
| L16-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 21-Jul-14 | 22-Jul-14 | 70 |
| L16-7110 | HVAC Firestop & Inspect (2) | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 110 |
| LL2E-8108 | LL2 - Set fire pumps and equipment | 5 | 5 | 22-Jul-14 | 28-Jul-14 | 34 |
| L07-6005 | CMU Fire Caulk/Clips | 2 | 2 | 22-Jul-14 | 23-Jul-14 | 4 |
| L12-6223 | Frame Corridor Ceilings | 2 | 2 | 22-Jul-14 | 23-Jul-14 | 21 |
| L03-8129 | Install Shower Doors | 5 | 5 | 22-Jul-14 | 28-Jul-14 | 57 |
| L05-7018 | Electrical Rough-In | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 67 |
| L06-7018 | Electrical Rough-In | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 67 |
| L07-7018 | Electrical Rough-In | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 67 |
| L08-7018 | Electrical Rough-In | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 67 |
| L09-7018 | Electrical Rough-In | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 67 |

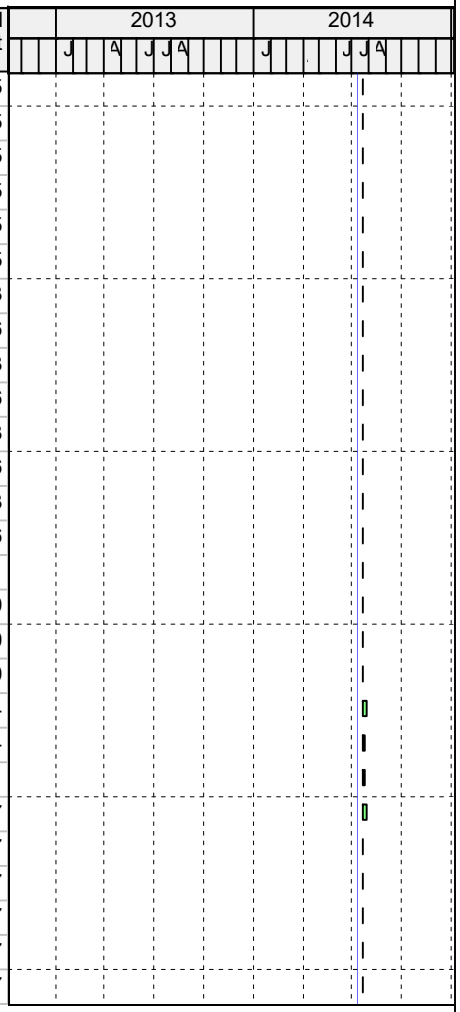



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7018 | Electrical Rough-In | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 67 |
| L11-7018 | Electrical Rough-In | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 67 |
| L12-7018 | Electrical Rough-In | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 67 |
| L14-7018 | Electrical Rough-In | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 67 |
| L17-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 22-Jul-14 | 23-Jul-14 | 63 |
| L17-7008 | HVAC Firestop & Inspect (2) | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 63 |
| L07-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 75 |
| L08-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 75 |
| L09-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 75 |
| L10-7120 | Electrical Rough-In | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 73 |
| L11-7120 | Electrical Rough-In | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 73 |
| L12-7120 | Electrical Rough-In | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 73 |
| L14-7120 | Electrical Rough-In | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 73 |
| L16-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 22-Jul-14 | 23-Jul-14 | 70 |
| L16-7114 | HVAC Firestop & Inspect (3) | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 109 |
| L17-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 22-Jul-14 | 23-Jul-14 | 69 |
| L17-7110 | HVAC Firestop & Inspect (2) | 1 | 1 | 22-Jul-14 | 22-Jul-14 | 109 |
| I-2502 | Electrical rework at LL1 for ASIs 7, 9r2, 14, 27 | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 23 |
| L16-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 23-Jul-14 | 24-Jul-14 | 32 |
| L16-6036 | Framing Around Heat Pump & Soffit | 3 | 3 | 23-Jul-14 | 25-Jul-14 | 30 |
| L1B-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 10 | 23-Jul-14 | 05-Aug-14 | 24 |
| L04-7020 | HVAC Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 68 |
| L05-7020 | HVAC Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |
| L05-7022 | Fire Sprinkler Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |
| L06-7020 | HVAC Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |
| L06-7022 | Fire Sprinkler Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |
| L07-7020 | HVAC Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |

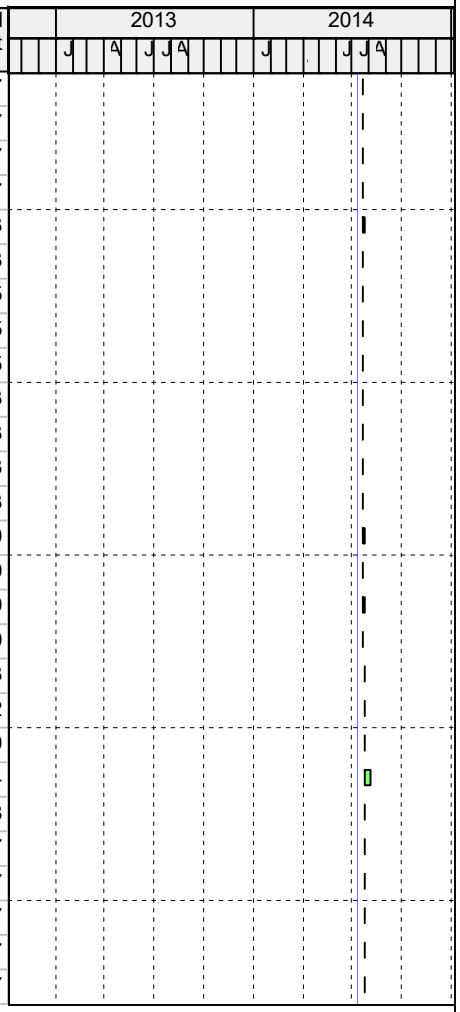



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7022 | Fire Sprinkler Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |
| L08-7020 | HVAC Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |
| L08-7022 | Fire Sprinkler Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |
| L09-7020 | HVAC Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |
| L09-7022 | Fire Sprinkler Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |
| L10-7020 | HVAC Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |
| L10-7022 | Fire Sprinkler Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |
| L11-7020 | HVAC Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |
| L11-7022 | Fire Sprinkler Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |
| L12-7020 | HVAC Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |
| L12-7022 | Fire Sprinkler Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |
| L14-7020 | HVAC Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |
| L14-7022 | Fire Sprinkler Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 67 |
| L15-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 65 |
| L15-7016 | Install HM door frame | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 68 |
| L16-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 65 |
| L16-7016 | Install HM door frame | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 68 |
| L17-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 23-Jul-14 | 24-Jul-14 | 63 |
| L17-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 64 |
| L07-7128 | Inspections for GWB Cover | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 75 |
| L08-7128 | Inspections for GWB Cover | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 75 |
| L09-7128 | Inspections for GWB Cover | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 75 |
| L10-7122 | HVAC Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 73 |
| L10-7124 | Fire Sprinkler Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 73 |
| L11-7122 | HVAC Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 73 |
| L11-7124 | Fire Sprinkler Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 73 |
| L12-7122 | HVAC Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 73 |

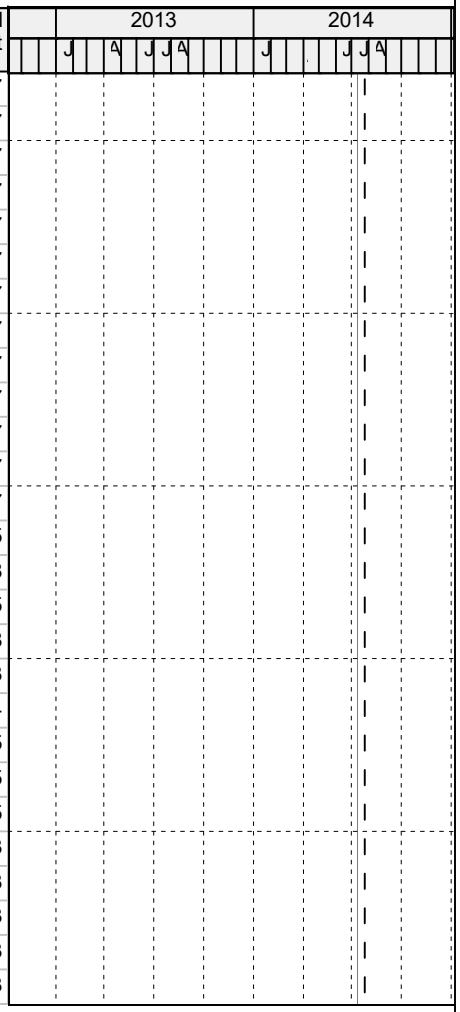



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7124 | Fire Sprinkler Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 73 |
| L14-7122 | HVAC Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 73 |
| L14-7124 | Fire Sprinkler Rough-In | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 73 |
| L15-7116 | Frame Walls | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 71 |
| L15-7118 | Install HM Door Frame | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 74 |
| L17-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 23-Jul-14 | 24-Jul-14 | 69 |
| L17-7114 | HVAC Firestop & Inspect (3) | 1 | 1 | 23-Jul-14 | 23-Jul-14 | 108 |
| L08-6005 | CMU Fire Caulk/Clips | 2 | 2 | 24-Jul-14 | 25-Jul-14 | 4 |
| L03-7030 | Paint | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 74 |
| L04-7026 | Inspections for GWB Cover | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 68 |
| L05-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 67 |
| L06-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 67 |
| L07-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 67 |
| L08-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 67 |
| L09-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 67 |
| L10-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 67 |
| L11-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 67 |
| L12-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 67 |
| L14-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 67 |
| L15-7018 | Electrical Rough-In | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 65 |
| L16-7018 | Electrical Rough-In | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 65 |
| L10-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 73 |
| L11-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 73 |
| L12-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 73 |
| L14-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 73 |
| L15-7120 | Electrical Rough-In | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 71 |
| L16-7116 | Frame Walls | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 70 |

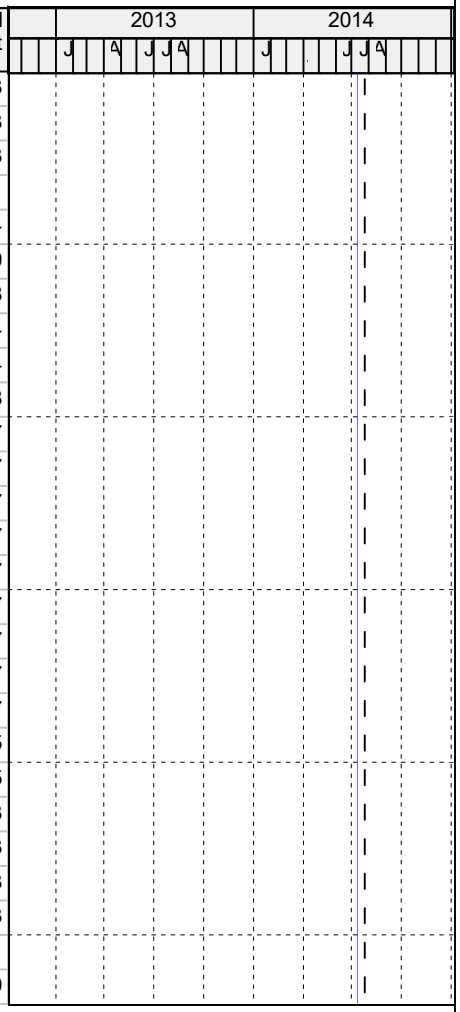



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-7118 | Install HM Door Frame | 1 | 1 | 24-Jul-14 | 24-Jul-14 | 73 |
| RF-4008 | Tower Roof - Coping / Flashing | 10 | 10 | 25-Jul-14 | 07-Aug-14 | 87 |
| L14-6223 | Frame Corridor Ceilings | 2 | 2 | 25-Jul-14 | 28-Jul-14 | 22 |
| L03-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 25-Jul-14 | 31-Jul-14 | 57 |
| L04-8129 | Install Shower Doors | 5 | 5 | 25-Jul-14 | 31-Jul-14 | 54 |
| L03-7032 | Install VCT Flooring (x42) | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 74 |
| L04-7028 | GWB Hang/Tape/Finish | 5 | 5 | 25-Jul-14 | 31-Jul-14 | 68 |
| L05-7026 | Inspections for GWB Cover | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 67 |
| L06-7026 | Inspections for GWB Cover | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 67 |
| L07-7026 | Inspections for GWB Cover | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 67 |
| L08-7026 | Inspections for GWB Cover | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 67 |
| L09-7026 | Inspections for GWB Cover | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 67 |
| L10-7026 | Inspections for GWB Cover | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 67 |
| L11-7026 | Inspections for GWB Cover | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 67 |
| L12-7026 | Inspections for GWB Cover | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 67 |
| L14-7026 | Inspections for GWB Cover | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 67 |
| L15-7020 | HVAC Rough-In | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 65 |
| L15-7022 | Fire Sprinkler Rough-In | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 65 |
| L16-7020 | HVAC Rough-In | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 65 |
| L16-7022 | Fire Sprinkler Rough-In | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 65 |
| L17-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 63 |
| L17-7016 | Install HM door frame | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 66 |
| L10-7128 | Inspections for GWB Cover | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 73 |
| L11-7128 | Inspections for GWB Cover | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 73 |
| L12-7128 | Inspections for GWB Cover | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 73 |
| L14-7128 | Inspections for GWB Cover | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 73 |
| L15-7122 | HVAC Rough-In | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 71 |

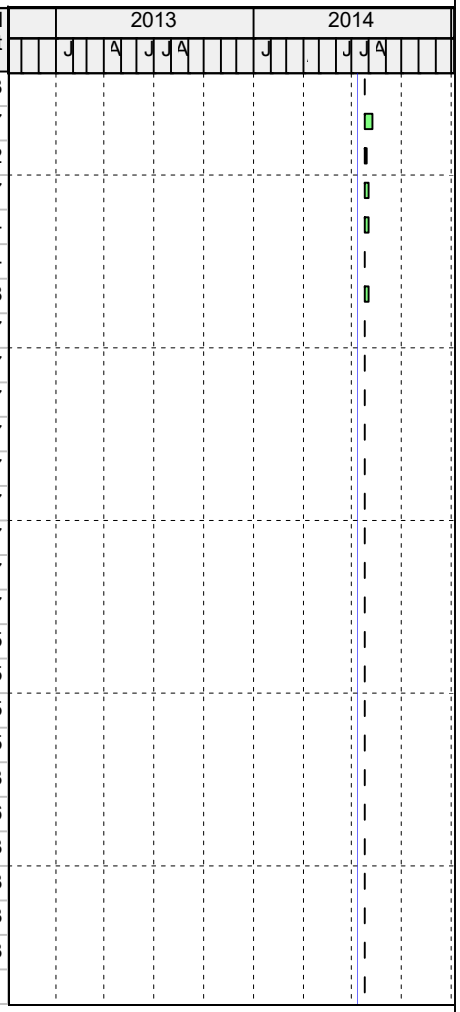



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-7124 | Fire Sprinkler Rough-In | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 71 |
| L16-7120 | Electrical Rough-In | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 70 |
| L17-7116 | Frame Walls | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 69 |
| L17-7118 | Install HM Door Frame | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 72 |
| L16-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 28-Jul-14 | 28-Jul-14 | 30 |
| L09-6005 | CMU Fire Caulk/Clips | 2 | 2 | 28-Jul-14 | 29-Jul-14 | 4 |
| L03-7034 | Install Door and Hardware (x42) | 1 | 1 | 28-Jul-14 | 28-Jul-14 | 74 |
| L03-7132 | Paint | 1 | 1 | 28-Jul-14 | 28-Jul-14 | 78 |
| L05-7028 | GWB Hang/Tape/Finish | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 67 |
| L06-7028 | GWB Hang/Tape/Finish | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 67 |
| L07-7028 | GWB Hang/Tape/Finish | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 67 |
| L08-7028 | GWB Hang/Tape/Finish | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 67 |
| L09-7028 | GWB Hang/Tape/Finish | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 67 |
| L10-7028 | GWB Hang/Tape/Finish | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 67 |
| L11-7028 | GWB Hang/Tape/Finish | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 67 |
| L12-7028 | GWB Hang/Tape/Finish | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 67 |
| L14-7028 | GWB Hang/Tape/Finish | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 67 |
| L15-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 28-Jul-14 | 28-Jul-14 | 65 |
| L16-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 28-Jul-14 | 28-Jul-14 | 65 |
| L17-7018 | Electrical Rough-In | 1 | 1 | 28-Jul-14 | 28-Jul-14 | 63 |
| L04-7132 | Paint | 1 | 1 | 28-Jul-14 | 28-Jul-14 | 78 |
| L05-7132 | Paint | 1 | 1 | 28-Jul-14 | 28-Jul-14 | 78 |
| L06-7132 | Paint | 1 | 1 | 28-Jul-14 | 28-Jul-14 | 78 |
| L07-7130 | GWB Hang/Tape/Finish | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 73 |
| L08-7130 | GWB Hang/Tape/Finish | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 73 |
| L09-7130 | GWB Hang/Tape/Finish | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 73 |
| L10-7130 | GWB Hang/Tape/Finish | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 73 |

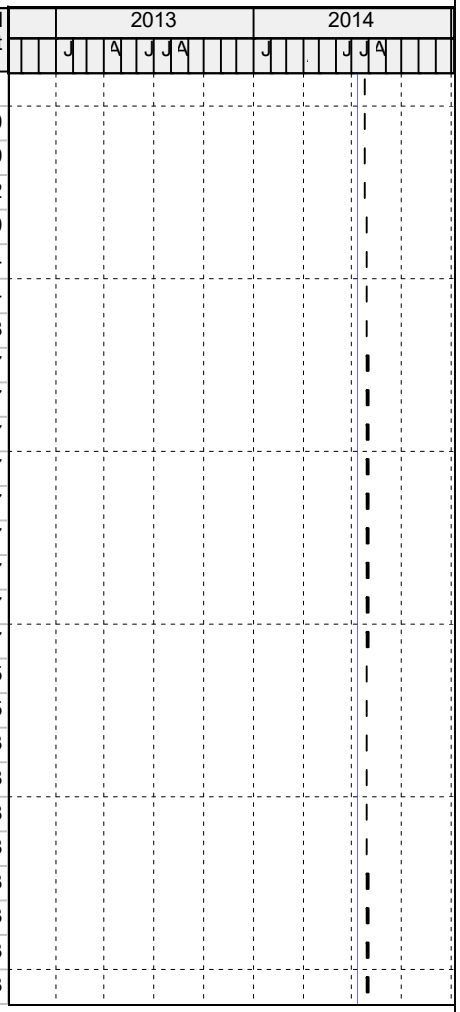



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7130 | GWB Hang/Tape/Finish | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 73 |
| L12-7130 | GWB Hang/Tape/Finish | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 73 |
| L14-7130 | GWB Hang/Tape/Finish | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 73 |
| L15-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 28-Jul-14 | 28-Jul-14 | 71 |
| L16-7122 | HVAC Rough-In | 1 | 1 | 28-Jul-14 | 28-Jul-14 | 70 |
| L16-7124 | Fire Sprinkler Rough-In | 1 | 1 | 28-Jul-14 | 28-Jul-14 | 70 |
| L17-7120 | Electrical Rough-In | 1 | 1 | 28-Jul-14 | 28-Jul-14 | 69 |
| MPP-1000 | Podium - West Elevation Grid X-FF Metal Panels | 5 | 5 | 29-Jul-14 | 04-Aug-14 | 70 |
| MPT-1000 | Tower - Initial West Elevation Metal Panels | 15 | 15 | 29-Jul-14 | 18-Aug-14 | 50 |
| MPP-1008 | Podium - East Elevation Metal Panels | 10 | 10 | 29-Jul-14 | 11-Aug-14 | 85 |
| MPT-1006 | Tower - East Elevation Grid FF-S Metal Panels | 15 | 15 | 29-Jul-14 | 18-Aug-14 | 50 |
| L03-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 29-Jul-14 | 31-Jul-14 | 74 |
| L03-7134 | Install VCT Flooring | 1 | 1 | 29-Jul-14 | 29-Jul-14 | 78 |
| L15-7026 | Inspections for GWB Cover | 1 | 1 | 29-Jul-14 | 29-Jul-14 | 65 |
| L16-7026 | Inspections for GWB Cover | 1 | 1 | 29-Jul-14 | 29-Jul-14 | 65 |
| L17-7020 | HVAC Rough-In | 1 | 1 | 29-Jul-14 | 29-Jul-14 | 63 |
| L17-7022 | Fire Sprinkler Rough-In | 1 | 1 | 29-Jul-14 | 29-Jul-14 | 63 |
| L04-7134 | Install VCT Flooring | 1 | 1 | 29-Jul-14 | 29-Jul-14 | 78 |
| L05-7134 | Install VCT Flooring | 1 | 1 | 29-Jul-14 | 29-Jul-14 | 78 |
| L06-7134 | Install VCT Flooring | 1 | 1 | 29-Jul-14 | 29-Jul-14 | 78 |
| L15-7128 | Inspections for GWB Cover | 1 | 1 | 29-Jul-14 | 29-Jul-14 | 71 |
| L16-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 29-Jul-14 | 29-Jul-14 | 70 |
| L17-7122 | HVAC Rough-In | 1 | 1 | 29-Jul-14 | 29-Jul-14 | 69 |
| L17-7124 | Fire Sprinkler Rough-In | 1 | 1 | 29-Jul-14 | 29-Jul-14 | 69 |
| L10-6005 | CMU Fire Caulk/Clips | 2 | 2 | 30-Jul-14 | 31-Jul-14 | 4 |
| L04-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 54 |
| L03-7136 | Install Door and Hardware | 1 | 1 | 30-Jul-14 | 30-Jul-14 | 78 |

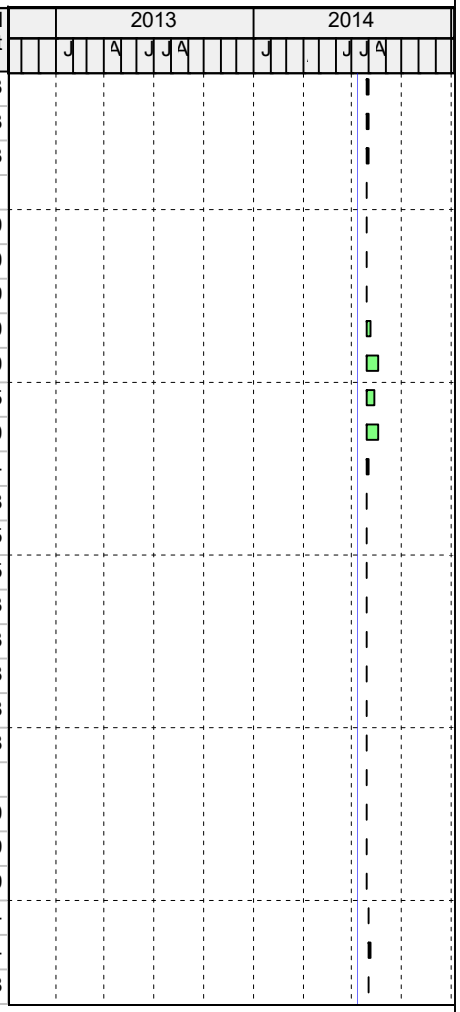



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-7028 | GWB Hang/Tape/Finish | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 65 |
| L16-7028 | GWB Hang/Tape/Finish | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 65 |
| L17-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 30-Jul-14 | 30-Jul-14 | 63 |
| L04-7136 | Install Door and Hardware | 1 | 1 | 30-Jul-14 | 30-Jul-14 | 78 |
| L05-7136 | Install Door and Hardware | 1 | 1 | 30-Jul-14 | 30-Jul-14 | 78 |
| L06-7136 | Install Door and Hardware | 1 | 1 | 30-Jul-14 | 30-Jul-14 | 78 |
| L15-7130 | GWB Hang/Tape/Finish | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 71 |
| L16-7128 | Inspections for GWB Cover | 1 | 1 | 30-Jul-14 | 30-Jul-14 | 70 |
| L17-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 30-Jul-14 | 30-Jul-14 | 69 |
| L03-7138 | Electrical Trim-Out | 2 | 2 | 31-Jul-14 | 01-Aug-14 | 78 |
| L17-7026 | Inspections for GWB Cover | 1 | 1 | 31-Jul-14 | 31-Jul-14 | 63 |
| L04-7138 | Electrical Trim-Out | 2 | 2 | 31-Jul-14 | 01-Aug-14 | 78 |
| L05-7138 | Electrical Trim-Out | 2 | 2 | 31-Jul-14 | 01-Aug-14 | 78 |
| L06-7138 | Electrical Trim-Out | 2 | 2 | 31-Jul-14 | 01-Aug-14 | 78 |
| L16-7130 | GWB Hang/Tape/Finish | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 70 |
| L17-7128 | Inspections for GWB Cover | 1 | 1 | 31-Jul-14 | 31-Jul-14 | 69 |
| L03-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 01-Aug-14 | 08-Aug-14 | 20 |
| L04-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 01-Aug-14 | 08-Aug-14 | 20 |
| LL1-Z4-8090 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 01-Aug-14 | 08-Aug-14 | 54 |
| L11-6005 | CMU Fire Caulk/Clips | 2 | 2 | 01-Aug-14 | 04-Aug-14 | 4 |
| L03-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 01-Aug-14 | 04-Aug-14 | 74 |
| L04-7030 | Paint | 1 | 1 | 01-Aug-14 | 01-Aug-14 | 68 |
| L17-7028 | GWB Hang/Tape/Finish | 5 | 5 | 01-Aug-14 | 07-Aug-14 | 63 |
| L17-7130 | GWB Hang/Tape/Finish | 5 | 5 | 01-Aug-14 | 07-Aug-14 | 69 |
| L03-8201 | Wall Finishes @ Corridors | 4 | 4 | 04-Aug-14 | 07-Aug-14 | 74 |
| L05-8129 | Install Shower Doors | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 48 |
| L03-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 78 |

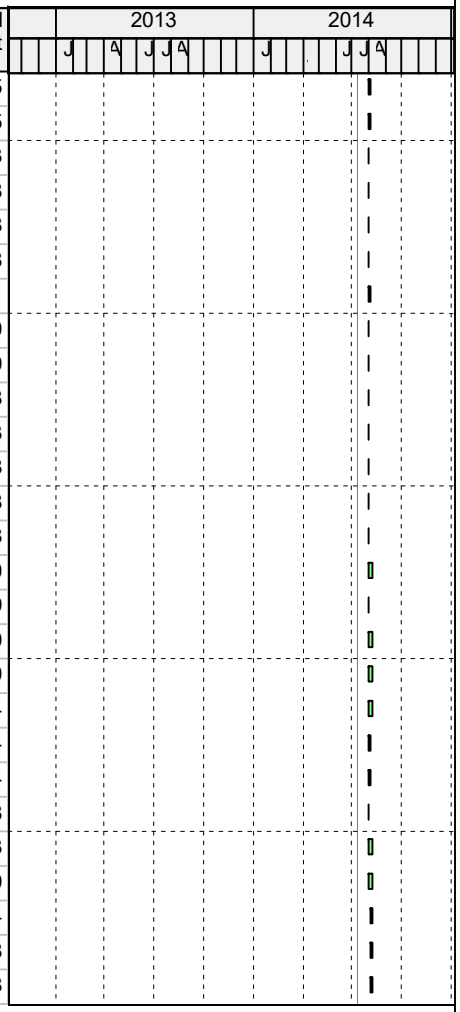



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7032 | Install VCT Flooring (x42) | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 68 |
| L05-7030 | Paint | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 67 |
| L06-7030 | Paint | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 67 |
| L07-7030 | Paint | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 67 |
| L08-7030 | Paint | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 67 |
| L09-7030 | Paint | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 67 |
| L10-7030 | Paint | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 67 |
| L11-7030 | Paint | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 67 |
| L12-7030 | Paint | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 67 |
| L14-7030 | Paint | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 67 |
| L04-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 78 |
| L05-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 78 |
| L06-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 78 |
| L07-7132 | Paint | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 73 |
| L08-7132 | Paint | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 73 |
| L09-7132 | Paint | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 73 |
| L10-7132 | Paint | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 73 |
| L11-7132 | Paint | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 73 |
| L12-7132 | Paint | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 73 |
| L14-7132 | Paint | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 73 |
| MPP-1002 | Podium - South Elevation Grid 18-15 Metal Panels | 2 | 2 | 05-Aug-14 | 06-Aug-14 | 70 |
| L12-6005 | CMU Fire Caulk/Clips | 2 | 2 | 05-Aug-14 | 06-Aug-14 | 4 |
| L03-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 74 |
| L04-7034 | Install Door and Hardware (x42) | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 68 |
| L05-7032 | Install VCT Flooring (x42) | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 67 |
| L06-7032 | Install VCT Flooring (x42) | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 67 |
| L07-7032 | Install VCT Flooring (x42) | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 67 |

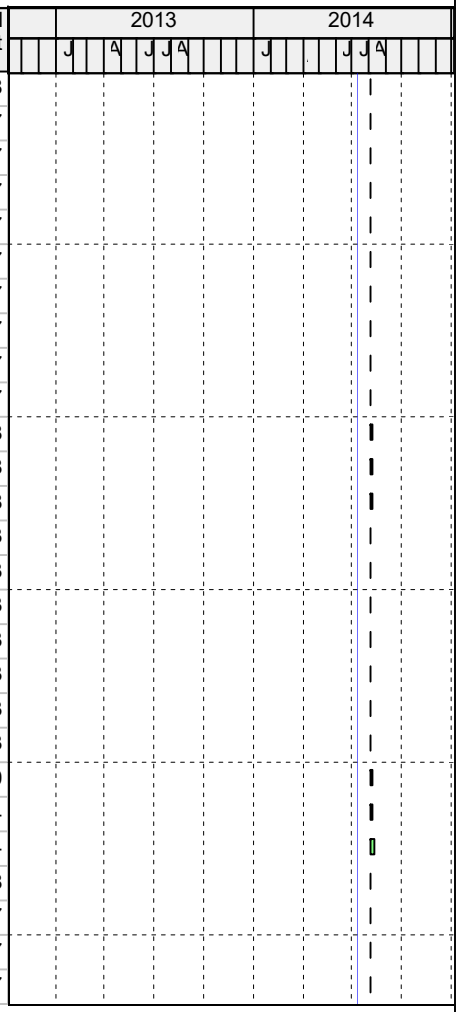



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7032 | Install VCT Flooring (x42) | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 67 |
| L09-7032 | Install VCT Flooring (x42) | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 67 |
| L10-7032 | Install VCT Flooring (x42) | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 67 |
| L11-7032 | Install VCT Flooring (x42) | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 67 |
| L12-7032 | Install VCT Flooring (x42) | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 67 |
| L14-7032 | Install VCT Flooring (x42) | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 67 |
| L07-7134 | Install VCT Flooring | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 73 |
| L08-7134 | Install VCT Flooring | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 73 |
| L09-7134 | Install VCT Flooring | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 73 |
| L10-7134 | Install VCT Flooring | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 73 |
| L11-7134 | Install VCT Flooring | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 73 |
| L12-7134 | Install VCT Flooring | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 73 |
| L14-7134 | Install VCT Flooring | 1 | 1 | 05-Aug-14 | 05-Aug-14 | 73 |
| L04-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 06-Aug-14 | 08-Aug-14 | 68 |
| L05-7034 | Install Door and Hardware (x42) | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 67 |
| L06-7034 | Install Door and Hardware (x42) | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 67 |
| L07-7034 | Install Door and Hardware (x42) | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 67 |
| L08-7034 | Install Door and Hardware (x42) | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 67 |
| L09-7034 | Install Door and Hardware (x42) | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 67 |
| L10-7034 | Install Door and Hardware (x42) | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 67 |
| L11-7034 | Install Door and Hardware (x42) | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 67 |
| L12-7034 | Install Door and Hardware (x42) | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 67 |
| L14-7034 | Install Door and Hardware (x42) | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 67 |
| L15-7030 | Paint | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 65 |
| L16-7030 | Paint | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 65 |
| L07-7136 | Install Door and Hardware | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 73 |
| L08-7136 | Install Door and Hardware | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 73 |

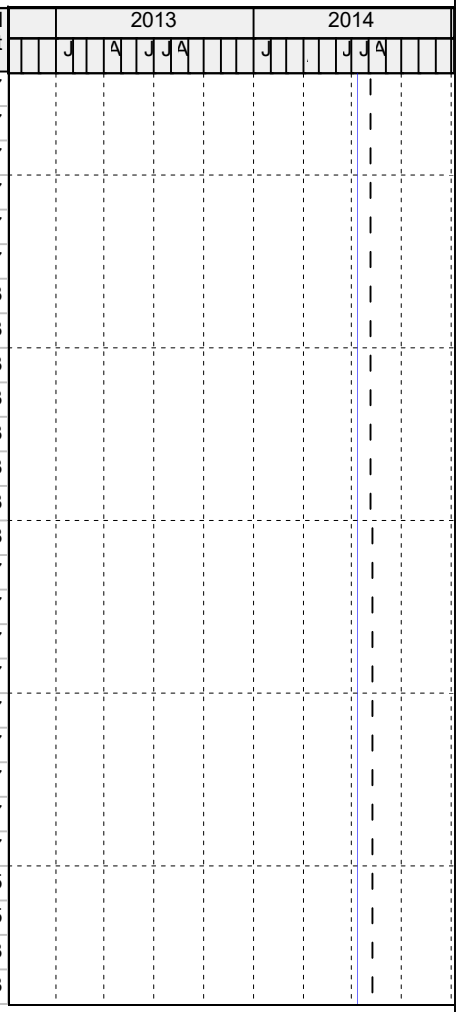



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-7136 | Install Door and Hardware | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 73 |
| L10-7136 | Install Door and Hardware | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 73 |
| L11-7136 | Install Door and Hardware | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 73 |
| L12-7136 | Install Door and Hardware | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 73 |
| L14-7136 | Install Door and Hardware | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 73 |
| L15-7132 | Paint | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 71 |
| MPP-1004 | Podium - South Elevation Grid 13-1 Metal Panels | 4 | 4 | 07-Aug-14 | 12-Aug-14 | 70 |
| L14-6005 | CMU Fire Caulk/Clips | 2 | 2 | 07-Aug-14 | 08-Aug-14 | 4 |
| L04-8201 | Wall Finishes @ Corridors | 4 | 4 | 07-Aug-14 | 12-Aug-14 | 71 |
| L05-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 48 |
| L05-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 07-Aug-14 | 11-Aug-14 | 67 |
| L06-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 07-Aug-14 | 11-Aug-14 | 67 |
| L07-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 07-Aug-14 | 11-Aug-14 | 67 |
| L08-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 07-Aug-14 | 11-Aug-14 | 67 |
| L09-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 07-Aug-14 | 11-Aug-14 | 67 |
| L10-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 07-Aug-14 | 11-Aug-14 | 67 |
| L11-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 07-Aug-14 | 11-Aug-14 | 67 |
| L12-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 07-Aug-14 | 11-Aug-14 | 67 |
| L14-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 07-Aug-14 | 11-Aug-14 | 67 |
| L15-7032 | Install VCT Flooring (x42) | 1 | 1 | 07-Aug-14 | 07-Aug-14 | 65 |
| L16-7032 | Install VCT Flooring (x42) | 1 | 1 | 07-Aug-14 | 07-Aug-14 | 65 |
| L07-7138 | Electrical Trim-Out | 2 | 2 | 07-Aug-14 | 08-Aug-14 | 73 |
| L08-7138 | Electrical Trim-Out | 2 | 2 | 07-Aug-14 | 08-Aug-14 | 73 |
| L09-7138 | Electrical Trim-Out | 2 | 2 | 07-Aug-14 | 08-Aug-14 | 73 |
| L10-7138 | Electrical Trim-Out | 2 | 2 | 07-Aug-14 | 08-Aug-14 | 73 |
| L11-7138 | Electrical Trim-Out | 2 | 2 | 07-Aug-14 | 08-Aug-14 | 73 |
| L12-7138 | Electrical Trim-Out | 2 | 2 | 07-Aug-14 | 08-Aug-14 | 73 |

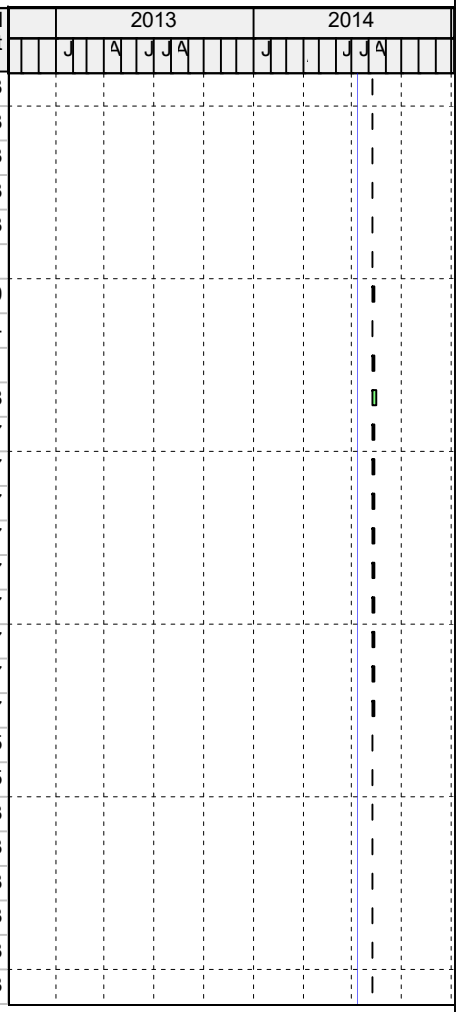



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-7138 | Electrical Trim-Out | 2 | 2 | 07-Aug-14 | 08-Aug-14 | 73 |
| L15-7134 | Install VCT Flooring | 1 | 1 | 07-Aug-14 | 07-Aug-14 | 71 |
| L16-7132 | Paint | 1 | 1 | 07-Aug-14 | 07-Aug-14 | 70 |
| L17-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 24 |
| L17-6040 | Test Heat Pumps - L15, L16 and L17 | 3 | 3 | 08-Aug-14 | 12-Aug-14 | 16 |
| L17-6036 | Framing Around Heat Pump & Soffit | 3 | 3 | 08-Aug-14 | 12-Aug-14 | 22 |
| L02-5102 | L2 - Storefront Frames | 3 | 3 | 08-Aug-14 | 12-Aug-14 | 21 |
| L06-8129 | Install Shower Doors | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 60 |
| L15-7034 | Install Door and Hardware (x42) | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 65 |
| L16-7034 | Install Door and Hardware (x42) | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 65 |
| L17-7030 | Paint | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 63 |
| L15-7136 | Install Door and Hardware | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 71 |
| L16-7134 | Install VCT Flooring | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 70 |
| L17-7132 | Paint | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 69 |
| L03-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 47 |
| L04-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 47 |
| LL1-Z4-8092 | Frame Ceilings/Furred Wall at Elevator Fronts | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 54 |
| L05-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 11-Aug-14 | 18-Aug-14 | 20 |
| L06-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 11-Aug-14 | 18-Aug-14 | 20 |
| L15-6005 | CMU Fire Caulk/Clips | 2 | 2 | 11-Aug-14 | 12-Aug-14 | 4 |
| L04-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 11-Aug-14 | 12-Aug-14 | 68 |
| L15-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 11-Aug-14 | 13-Aug-14 | 65 |
| L16-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 11-Aug-14 | 13-Aug-14 | 65 |
| L17-7032 | Install VCT Flooring (x42) | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 63 |
| L07-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 73 |
| L08-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 73 |
| L09-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 73 |

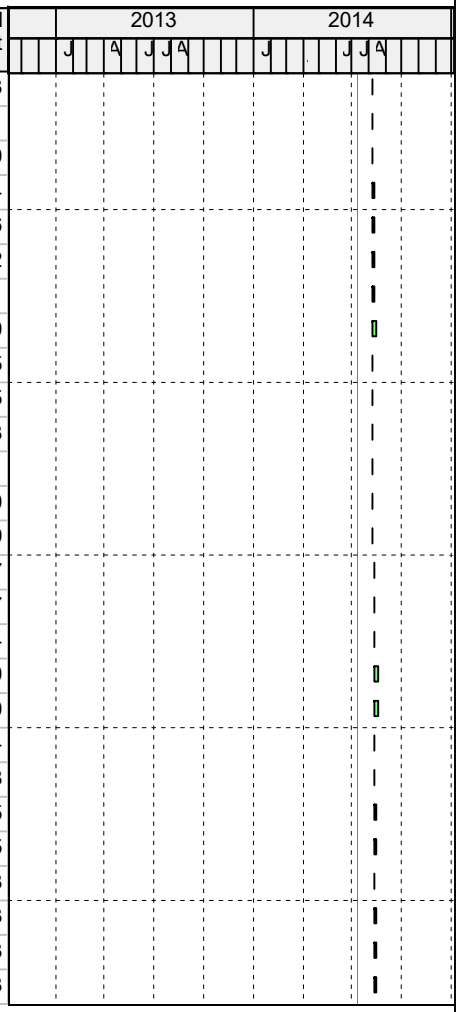



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 73 |
| L11-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 73 |
| L12-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 73 |
| L14-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 73 |
| L15-7138 | Electrical Trim-Out | 2 | 2 | 11-Aug-14 | 12-Aug-14 | 71 |
| L16-7136 | Install Door and Hardware | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 70 |
| L17-7134 | Install VCT Flooring | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 69 |
| L03-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 48 |
| L04-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 48 |
| L03-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 48 |
| L04-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 48 |
| LL1-Z4-8094 | Electrical Rough-In at Elevator Fronts/Ceiling | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 54 |
| MPP-1010 | Podium - North Elevation Metal Panels | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 85 |
| L03-7042 | Install Tile Flooring (x41) | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 74 |
| L05-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 67 |
| L06-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 67 |
| L07-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 67 |
| L08-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 67 |
| L09-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 67 |
| L10-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 67 |
| L11-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 67 |
| L12-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 67 |
| L14-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 67 |
| L17-7034 | Install Door and Hardware (x42) | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 63 |
| L16-7138 | Electrical Trim-Out | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 70 |
| L17-7136 | Install Door and Hardware | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 69 |
| L17-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 22 |

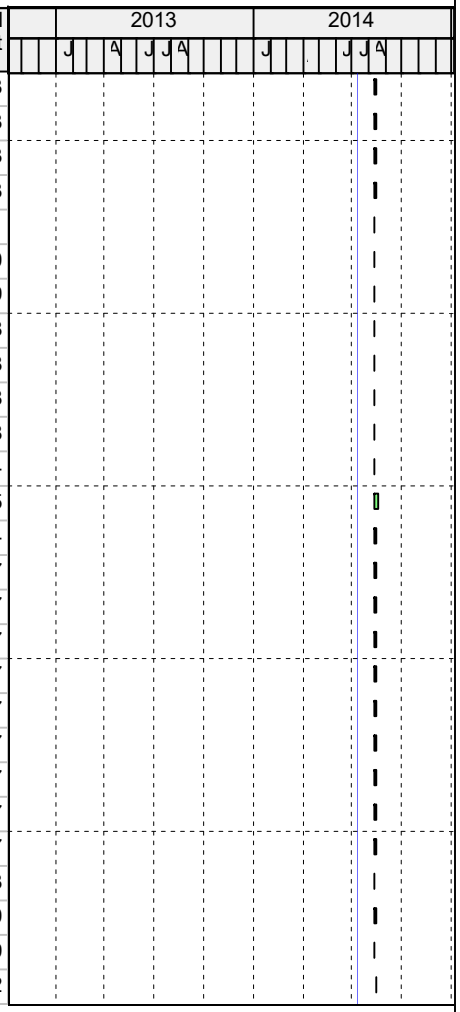



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 48 |
| L04-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 48 |
| L03-8405 | Cover Inspection | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 48 |
| L04-8405 | Cover Inspection | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 48 |
| LL1-Z4-8096 | Fire Sprinkler Rough-in at Elevatgor Fronts/Ceiling | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 54 |
| MPP-1006 | Podium and Ballroom - South Elevation Metal Panels | 10 | 10 | 13-Aug-14 | 26-Aug-14 | 70 |
| L02-5104 | L2 - Storefront Glazing | 2 | 2 | 13-Aug-14 | 14-Aug-14 | 21 |
| L16-6005 | CMU Fire Caulk/Clips | 2 | 2 | 13-Aug-14 | 14-Aug-14 | 6 |
| L06-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 60 |
| L04-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 68 |
| L17-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 13-Aug-14 | 15-Aug-14 | 63 |
| L15-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 71 |
| L17-7138 | Electrical Trim-Out | 2 | 2 | 13-Aug-14 | 14-Aug-14 | 69 |
| LL1-Z4-8098 | Cover Inspection | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 54 |
| L07-8129 | Install Shower Doors | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 56 |
| L03-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 74 |
| L05-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 67 |
| L06-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 67 |
| L07-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 67 |
| L08-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 67 |
| L09-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 67 |
| L10-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 67 |
| L11-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 67 |
| L12-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 67 |
| L14-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 67 |
| L15-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 14-Aug-14 | 15-Aug-14 | 65 |
| L16-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 14-Aug-14 | 15-Aug-14 | 65 |

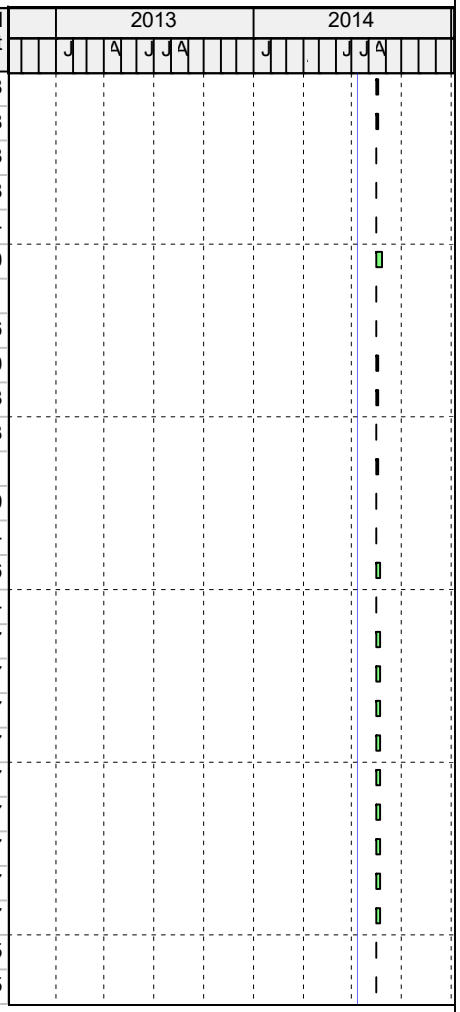



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 70 |
| L17-6005 | CMU Fire Caulk/Clips | 2 | 2 | 15-Aug-14 | 18-Aug-14 | 19 |
| L05-8201 | Wall Finishes @ Corridors | 4 | 4 | 15-Aug-14 | 20-Aug-14 | 65 |
| L17-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 69 |
| L15-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 65 |
| L16-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 65 |
| L17-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 18-Aug-14 | 19-Aug-14 | 63 |
| L1BOH1-8100 | Insulation | 2 | 2 | 19-Aug-14 | 20-Aug-14 | 43 |
| L03-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 48 |
| L05-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 42 |
| L06-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 57 |
| L04-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 48 |
| L07-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 19-Aug-14 | 26-Aug-14 | 20 |
| L08-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 19-Aug-14 | 26-Aug-14 | 20 |
| MPT-1002 | Tower - Complete West Elevation Metal Panels | 10 | 10 | 19-Aug-14 | 02-Sep-14 | 50 |
| MPT-1010 | Tower - East Elevation Gris S-A Metal Panels | 10 | 10 | 19-Aug-14 | 02-Sep-14 | 50 |
| L07-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 56 |
| L03-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 48 |
| L04-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 48 |
| L05-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 42 |
| L06-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 58 |
| L05-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 42 |
| L06-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 58 |
| L08-8129 | Install Shower Doors | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 52 |
| L04-7042 | Install Tile Flooring (x41) | 2 | 2 | 20-Aug-14 | 21-Aug-14 | 68 |
| L17-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 63 |
| L03-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 48 |

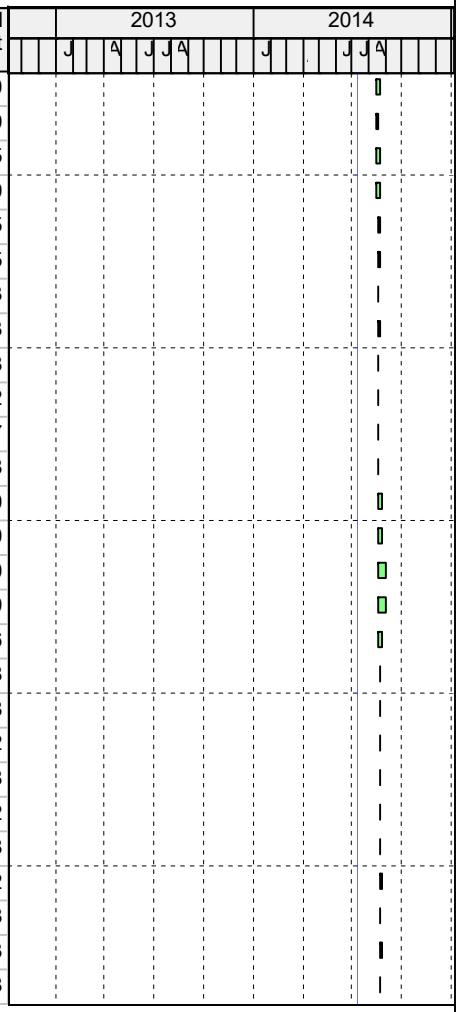



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 48 |
| L05-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 42 |
| L06-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 58 |
| L05-8405 | Cover Inspection | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 42 |
| L06-8405 | Cover Inspection | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 58 |
| L06-8201 | Wall Finishes @ Corridors | 4 | 4 | 21-Aug-14 | 26-Aug-14 | 61 |
| L05-7042 | Install Tile Flooring (x41) | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 67 |
| L06-7042 | Install Tile Flooring (x41) | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 67 |
| L07-7042 | Install Tile Flooring (x41) | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 67 |
| L08-7042 | Install Tile Flooring (x41) | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 67 |
| L09-7042 | Install Tile Flooring (x41) | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 67 |
| L10-7042 | Install Tile Flooring (x41) | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 67 |
| L11-7042 | Install Tile Flooring (x41) | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 67 |
| L12-7042 | Install Tile Flooring (x41) | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 67 |
| L14-7042 | Install Tile Flooring (x41) | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 67 |
| LL1-Z4-8100 | Insulation | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 49 |
| LL1-Z5-8100 | Insulation | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 30 |
| L15-6223 | Frame Corridor Ceilings | 2 | 2 | 22-Aug-14 | 25-Aug-14 | 6 |
| L04-7044 | Install Vending Cabinets (x41) | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 68 |
| LL1-Z6-8100 | Insulation | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 36 |
| L03-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 48 |
| L04-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 48 |
| L08-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 52 |
| L05-7044 | Install Vending Cabinets (x41) | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 67 |
| L06-7044 | Install Vending Cabinets (x41) | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 67 |
| L07-7044 | Install Vending Cabinets (x41) | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 67 |
| L08-7044 | Install Vending Cabinets (x41) | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 67 |





© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 67 |
| L10-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 67 |
| L11-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 67 |
| L12-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 67 |
| L14-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 67 |
| L15-7042 | Install Tile Flooring (x41) | 2 | 2 | 25-Aug-14 | 26-Aug-14 | 65 |
| L16-7042 | Install Tile Flooring (x41) | 2 | 2 | 25-Aug-14 | 26-Aug-14 | 65 |
| LL1-Z7-8100 | Insulation | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 38 |
| L03-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 48 |
| L03-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 48 |
| L04-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 48 |
| L04-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 48 |
| L09-8129 | Install Shower Doors | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 48 |
| L1BOH1-8102 | GWB Hang | 3 | 3 | 27-Aug-14 | 29-Aug-14 | 39 |
| L03-8418 | Flooring at Elevator Lobby | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 64 |
| L07-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 27-Aug-14 | 27-Aug-14 | 52 |
| L08-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 27-Aug-14 | 27-Aug-14 | 51 |
| L04-8418 | Flooring at Elevator Lobby | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 64 |
| L05-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 27-Aug-14 | 27-Aug-14 | 42 |
| L06-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 27-Aug-14 | 27-Aug-14 | 58 |
| L09-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 27-Aug-14 | 04-Sep-14 | 20 |
| L10-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 27-Aug-14 | 04-Sep-14 | 20 |
| MPL4-1000 | Upper L4 Ballroom - South Elevation Vertical Metal P: | 3 | 3 | 27-Aug-14 | 29-Aug-14 | 70 |
| L16-6223 | Frame Corridor Ceilings | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 7 |
| L07-8201 | Wall Finishes @ Corridors | 4 | 4 | 27-Aug-14 | 02-Sep-14 | 57 |
| L15-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 27-Aug-14 | 27-Aug-14 | 65 |
| L16-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 27-Aug-14 | 27-Aug-14 | 65 |

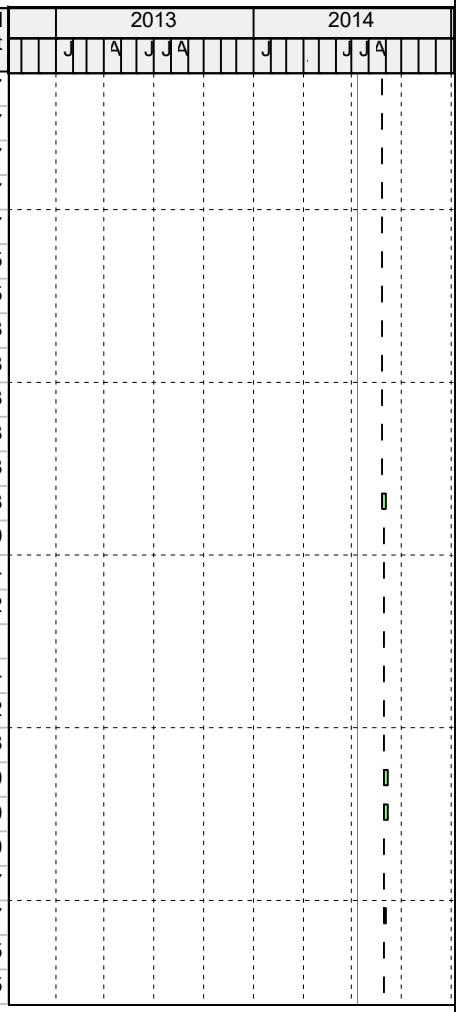



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7042 | Install Tile Flooring (x41) | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 63 |
| L05-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 42 |
| L06-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 58 |
| L07-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 52 |
| L08-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 52 |
| L07-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 52 |
| L08-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 52 |
| LL1-Z4-8102 | GWB Hang | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 45 |
| LL1-Z5-8102 | GWB Hang | 3 | 3 | 29-Aug-14 | 03-Sep-14 | 26 |
| L05-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 42 |
| L06-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 58 |
| L07-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 52 |
| L08-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 52 |
| L07-8405 | Cover Inspection | 1 | 1 | 29-Aug-14 | 29-Aug-14 | 52 |
| L08-8405 | Cover Inspection | 1 | 1 | 29-Aug-14 | 29-Aug-14 | 52 |
| L03-8612 | L3 Pool - GWB hang/tape/finish | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 41 |
| L09-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 48 |
| L17-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 29-Aug-14 | 29-Aug-14 | 63 |
| MPL4-1002 | Upper L4 Ballroom - West Elevation Vertical Metal Pa | 3 | 3 | 02-Sep-14 | 04-Sep-14 | 70 |
| L10-8129 | Install Shower Doors | 5 | 5 | 02-Sep-14 | 08-Sep-14 | 44 |
| LL1-Z4-8215 | GWB Tape | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 45 |
| L05-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 03-Sep-14 | 03-Sep-14 | 42 |
| L06-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 03-Sep-14 | 03-Sep-14 | 58 |
| MPT-1004 | Tower - South Elevation Grid 18-10 Metal Panels | 20 | 20 | 03-Sep-14 | 30-Sep-14 | 50 |
| MPT-1012 | Tower - North Elevation Grid 8-18 Metal Panels | 25 | 25 | 03-Sep-14 | 07-Oct-14 | 50 |
| I-4004 | East Stitched - Install metal panels | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 70 |
| L08-8201 | Wall Finishes @ Corridors | 4 | 4 | 03-Sep-14 | 08-Sep-14 | 53 |

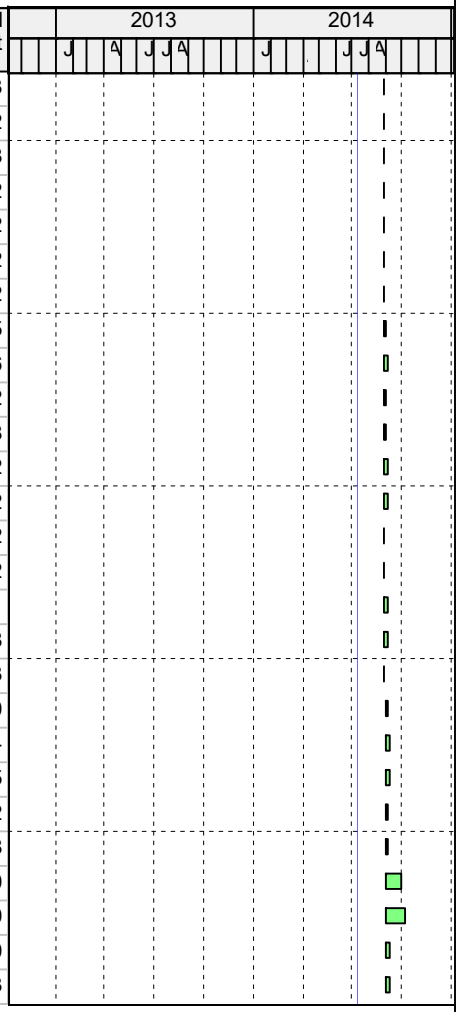



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z6-8102 | GWB Hang | 1 | 1 | 04-Sep-14 | 04-Sep-14 | 30 |
| L05-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 04-Sep-14 | 04-Sep-14 | 42 |
| L05-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 04-Sep-14 | 04-Sep-14 | 42 |
| L06-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 04-Sep-14 | 04-Sep-14 | 58 |
| L06-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 04-Sep-14 | 04-Sep-14 | 58 |
| L17-6223 | Frame Corridor Ceilings | 2 | 2 | 04-Sep-14 | 05-Sep-14 | 6 |
| LL1-Z7-8102 | GWB Hang | 3 | 3 | 05-Sep-14 | 09-Sep-14 | 32 |
| L09-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 05-Sep-14 | 05-Sep-14 | 46 |
| L10-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 05-Sep-14 | 05-Sep-14 | 45 |
| L05-8418 | Flooring at Elevator Lobby | 2 | 2 | 05-Sep-14 | 08-Sep-14 | 58 |
| L06-8418 | Flooring at Elevator Lobby | 2 | 2 | 05-Sep-14 | 08-Sep-14 | 58 |
| L07-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 05-Sep-14 | 05-Sep-14 | 52 |
| L08-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 05-Sep-14 | 05-Sep-14 | 52 |
| L11-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 05-Sep-14 | 12-Sep-14 | 20 |
| L12-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 05-Sep-14 | 12-Sep-14 | 20 |
| MPL4-1004 | Upper L4 Ballroom - North Elevation Vertical Metal Pa | 3 | 3 | 05-Sep-14 | 09-Sep-14 | 70 |
| L10-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 05-Sep-14 | 11-Sep-14 | 44 |
| L1BOH1-8215 | GWB Tape | 6 | 6 | 08-Sep-14 | 15-Sep-14 | 35 |
| L07-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 52 |
| L08-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 52 |
| L09-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 46 |
| L10-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 46 |
| L09-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 46 |
| L10-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 46 |
| L03-8614 | L3 Pool - Paint/wall finishes | 3 | 3 | 08-Sep-14 | 10-Sep-14 | 56 |
| L03-8618 | L3 Pool - Ceramic tile | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 54 |
| L11-8129 | Install Shower Doors | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 40 |

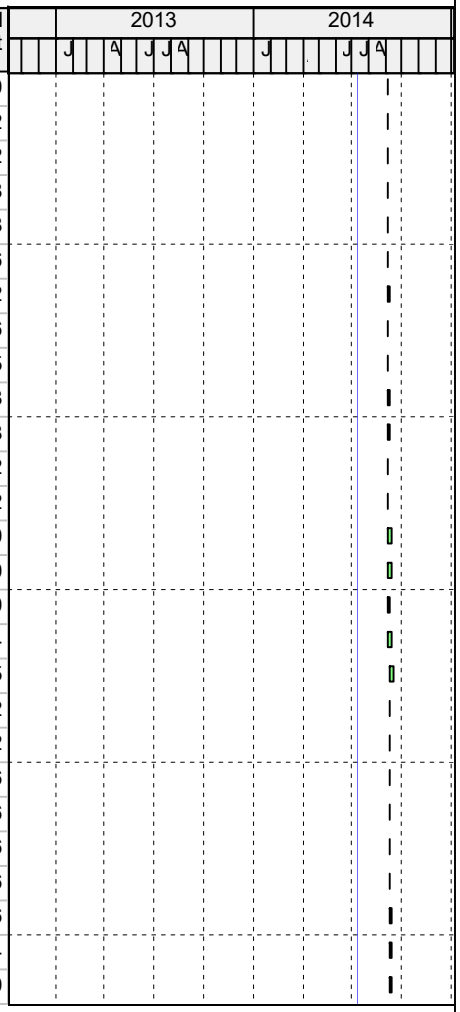



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 52 |
| L08-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 52 |
| L09-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 46 |
| L10-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 46 |
| LL1-Z2-8108 | Install Junior Balllroom ceiling feature (allowance) | 10 | 10 | 09-Sep-14 | 22-Sep-14 | 38 |
| L09-8405 | Cover Inspection | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 46 |
| L10-8405 | Cover Inspection | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 46 |
| L09-8201 | Wall Finishes @ Corridors | 4 | 4 | 09-Sep-14 | 12-Sep-14 | 49 |
| LL1-Z4-8104 | Prime Paint | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 45 |
| LL1-Z5-8215 | GWB Tape | 5 | 5 | 10-Sep-14 | 16-Sep-14 | 22 |
| L1RR-8100 | Insulation | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 20 |
| I-3102 | Ballroom ceilings - additional work per ASIs 18, 25 | 10 | 10 | 11-Sep-14 | 24-Sep-14 | 21 |
| L07-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 52 |
| L08-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 52 |
| L1B-8120 | Install operable partitions | 10 | 10 | 11-Sep-14 | 24-Sep-14 | 26 |
| L11-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 40 |
| L1BOH2-8100 | Insulation | 2 | 2 | 12-Sep-14 | 15-Sep-14 | 17 |
| LL1-Z4-8114 | T Bar Grid Ceiling | 1 | 1 | 12-Sep-14 | 12-Sep-14 | 45 |
| L07-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 12-Sep-14 | 12-Sep-14 | 52 |
| L07-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 12-Sep-14 | 12-Sep-14 | 52 |
| L08-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 12-Sep-14 | 12-Sep-14 | 52 |
| L08-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 12-Sep-14 | 12-Sep-14 | 52 |
| L12-8129 | Install Shower Doors | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 36 |
| LL1-Z4-8116 | Finish Carpentry / Millwork | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 45 |
| L11-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 40 |
| L12-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 39 |
| L07-8418 | Flooring at Elevator Lobby | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 52 |

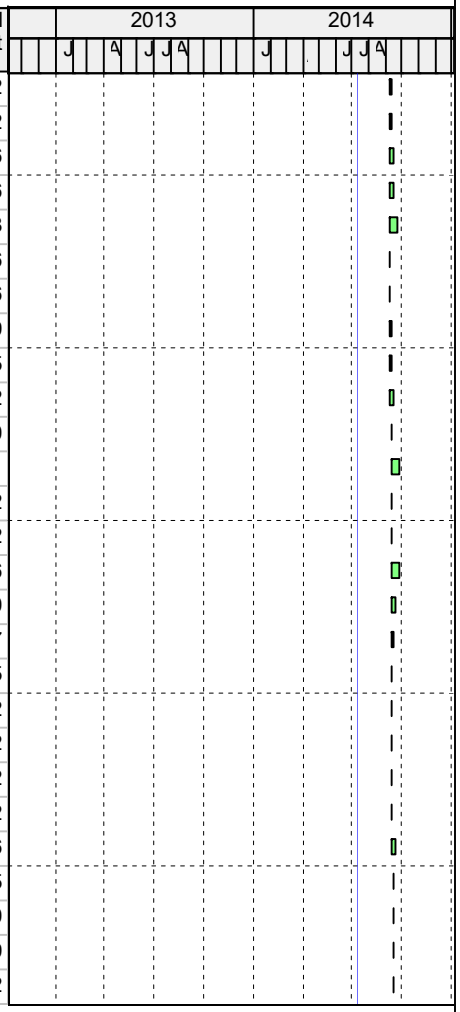



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8418 | Flooring at Elevator Lobby | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 52 |
| L09-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 46 |
| L10-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 46 |
| L14-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 15-Sep-14 | 22-Sep-14 | 20 |
| L15-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 15-Sep-14 | 22-Sep-14 | 20 |
| L03-8620 | L3 Pool - Plumbing Fixtures & Trim / Finish | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 54 |
| L03-8622 | L3 Pool - HVAC trim / Finish | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 54 |
| L03-8624 | L3 Pool - Fire Sprinkler Trim / Finish | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 54 |
| L03-8626 | L3 Pool - Elec Trim/ Finish | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 54 |
| L03-8628 | L3 Pool - Elec Specialties Trim / Finish | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 54 |
| L10-8201 | Wall Finishes @ Corridors | 4 | 4 | 15-Sep-14 | 18-Sep-14 | 45 |
| L1BOH1-8104 | Prime Paint | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 35 |
| L1BOH2-8102 | GWB Hang | 5 | 5 | 16-Sep-14 | 22-Sep-14 | 17 |
| L09-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 46 |
| L10-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 46 |
| L11-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 40 |
| L12-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 40 |
| L11-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 40 |
| L12-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 40 |
| LL1-Z4-8200 | First Coat Finish Paint | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 45 |
| LL1-Z5-8104 | Prime Paint | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 39 |
| LL1-Z6-8215 | GWB Tape | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 22 |
| L1RR-8102 | GWB Hang | 3 | 3 | 17-Sep-14 | 19-Sep-14 | 18 |
| L09-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 46 |
| L10-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 46 |
| L11-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 40 |
| L12-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 40 |

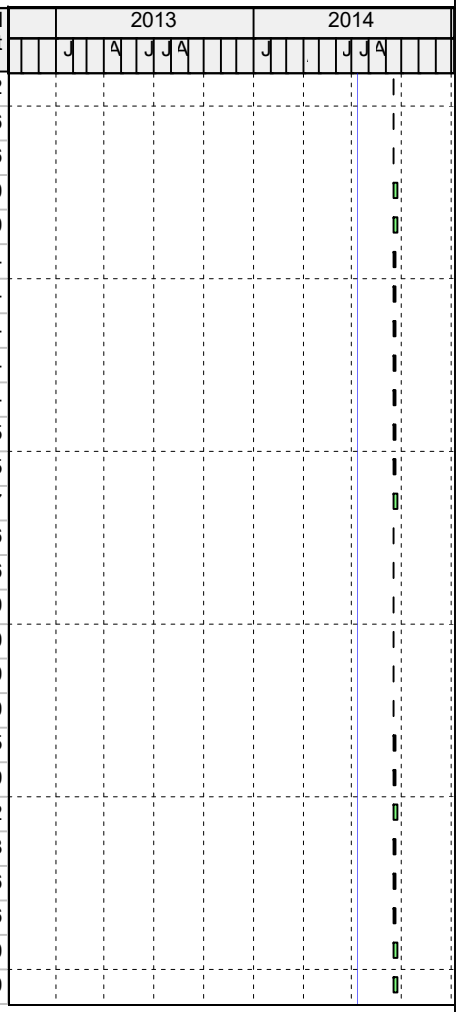



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8405 | Cover Inspection | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 40 |
| L12-8405 | Cover Inspection | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 40 |
| L12-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 36 |
| L1BOH1-8114 | T Bar Grid Ceiling | 3 | 3 | 18-Sep-14 | 22-Sep-14 | 35 |
| L14-8129 | Install Shower Doors | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 32 |
| LL1-Z4-8124 | Flooring | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 45 |
| LL1-Z5-8114 | T Bar Grid Ceiling | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 39 |
| L09-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 46 |
| L10-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 46 |
| L11-8201 | Wall Finishes @ Corridors | 4 | 4 | 19-Sep-14 | 24-Sep-14 | 41 |
| L09-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 46 |
| L09-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 46 |
| L10-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 46 |
| L10-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 46 |
| L03-8630 | L3 Pool - Doors & Hardware | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 54 |
| LL1-Z5-8116 | Finish Carpentry / Millwork | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 39 |
| LL1-Z4-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 48 |
| LL1-Z4-8126 | Doors & Hardware | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 45 |
| L1BOH1-8116 | Finish Carpentry / Millwork | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 35 |
| L1BOH2-8215 | GWB Tape | 7 | 7 | 23-Sep-14 | 01-Oct-14 | 17 |
| L14-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 34 |
| L15-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 26 |
| L09-8418 | Flooring at Elevator Lobby | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 46 |
| L10-8418 | Flooring at Elevator Lobby | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 46 |
| L11-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 40 |
| L12-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 40 |
| L16-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 23-Sep-14 | 30-Sep-14 | 20 |

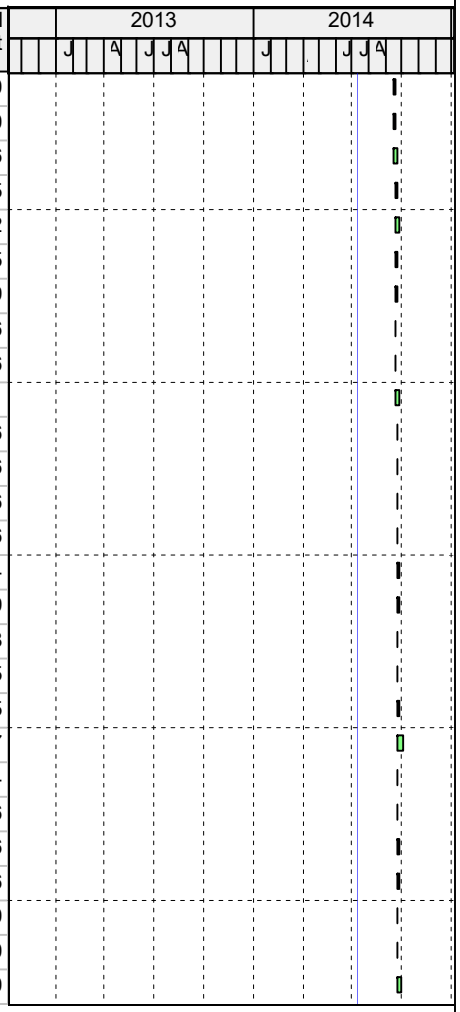



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 23-Sep-14 | 30-Sep-14 | 20 |
| L14-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 32 |
| LL1-Z6-8104 | Prime Paint | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 27 |
| LL1-Z7-8215 | GWB Tape | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 22 |
| LL1-Z4-8106 | Wallcoverings | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 45 |
| LL1-Z4-8201 | Final Coat Finish Paint | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 45 |
| L11-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 40 |
| L12-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 40 |
| L14-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 34 |
| L15-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 27 |
| L14-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 34 |
| L15-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 27 |
| L15-8129 | Install Shower Doors | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 12 |
| LL1-Z5-8200 | First Coat Finish Paint | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 39 |
| L1BOH1-8200 | First Coat Finish Paint | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 35 |
| L1RR-8215 | GWB Tape | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 15 |
| L11-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 40 |
| L12-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 40 |
| L14-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 34 |
| L15-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 27 |
| L14-8405 | Cover Inspection | 1 | 1 | 25-Sep-14 | 25-Sep-14 | 34 |
| L15-8405 | Cover Inspection | 1 | 1 | 25-Sep-14 | 25-Sep-14 | 27 |
| LL1-Z3-8340 | Install walk-in cooler/freezer (BY OTHERS) | 5 | 5 | 25-Sep-14* | 01-Oct-14 | 17 |
| L12-8201 | Wall Finishes @ Corridors | 4 | 4 | 25-Sep-14 | 30-Sep-14 | 40 |
| LL1-Z6-8114 | T Bar Grid Ceiling | 1 | 1 | 26-Sep-14 | 26-Sep-14 | 27 |
| LL1-Z4-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 26-Sep-14 | 29-Sep-14 | 46 |
| LL1-Z4-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 26-Sep-14 | 29-Sep-14 | 45 |

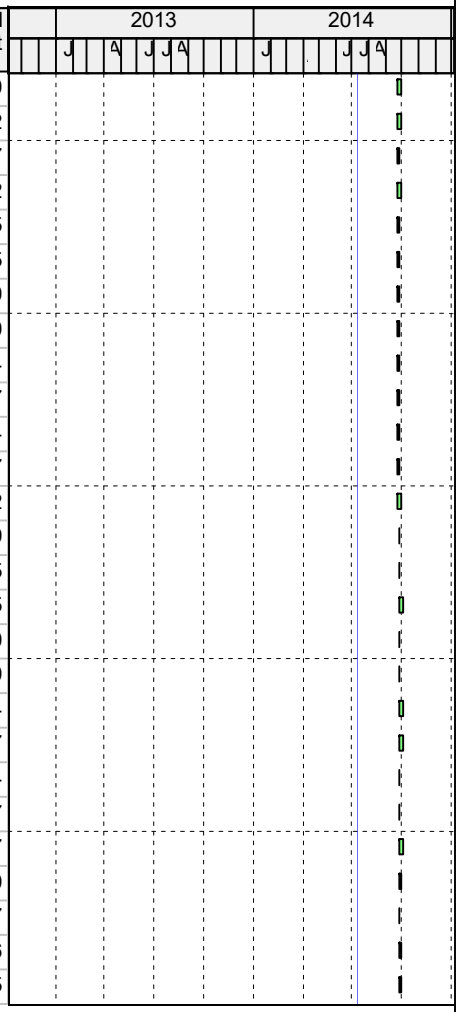



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z4-8204 | Mech Trim / Finish (HVAC) | 2 | 2 | 26-Sep-14 | 29-Sep-14 | 45 |
| LL1-Z5-8124 | Flooring | 3 | 3 | 29-Sep-14 | 01-Oct-14 | 39 |
| LL1-Z6-8116 | Finish Carpentry / Millwork | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 27 |
| L1BOH1-8124 | Flooring | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 35 |
| L11-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 29-Sep-14 | 29-Sep-14 | 40 |
| L12-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 29-Sep-14 | 29-Sep-14 | 40 |
| L03-8632 | L3 Pool - Install Bathroom Accessories | 3 | 3 | 29-Sep-14 | 01-Oct-14 | 54 |
| L15-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 12 |
| L11-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 30-Sep-14 | 30-Sep-14 | 40 |
| L11-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 30-Sep-14 | 30-Sep-14 | 40 |
| L12-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 30-Sep-14 | 30-Sep-14 | 40 |
| L12-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 30-Sep-14 | 30-Sep-14 | 40 |
| LL1-Z4-8140a | Acoustical Ceiling Tile (remainder) | 1 | 1 | 30-Sep-14 | 30-Sep-14 | 45 |
| L16-8129 | Install Shower Doors | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 8 |
| LL1-Z6-8200 | First Coat Finish Paint | 2 | 2 | 01-Oct-14 | 02-Oct-14 | 27 |
| LL1-Z7-8104 | Prime Paint | 3 | 3 | 01-Oct-14 | 03-Oct-14 | 22 |
| LL1-Z4-8134 | Pre-Clean | 1 | 1 | 01-Oct-14 | 01-Oct-14 | 45 |
| L1BOH1-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 1 | 1 | 01-Oct-14 | 01-Oct-14 | 41 |
| L1BOH1-8126 | Doors & Hardware | 1 | 1 | 01-Oct-14 | 01-Oct-14 | 35 |
| I-1102 | Additional work at new L17 guest rooms | 5 | 5 | 01-Oct-14 | 07-Oct-14 | 0 |
| L16-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 01-Oct-14 | 01-Oct-14 | 21 |
| L17-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 01-Oct-14 | 01-Oct-14 | 20 |
| L11-8418 | Flooring at Elevator Lobby | 2 | 2 | 01-Oct-14 | 02-Oct-14 | 40 |
| L12-8418 | Flooring at Elevator Lobby | 2 | 2 | 01-Oct-14 | 02-Oct-14 | 40 |
| L14-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 01-Oct-14 | 01-Oct-14 | 34 |
| L15-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 01-Oct-14 | 01-Oct-14 | 27 |
| MPT-1008 | Tower - South Elevation Grid 10-8 Metal Panels | 5 | 5 | 01-Oct-14 | 07-Oct-14 | 50 |

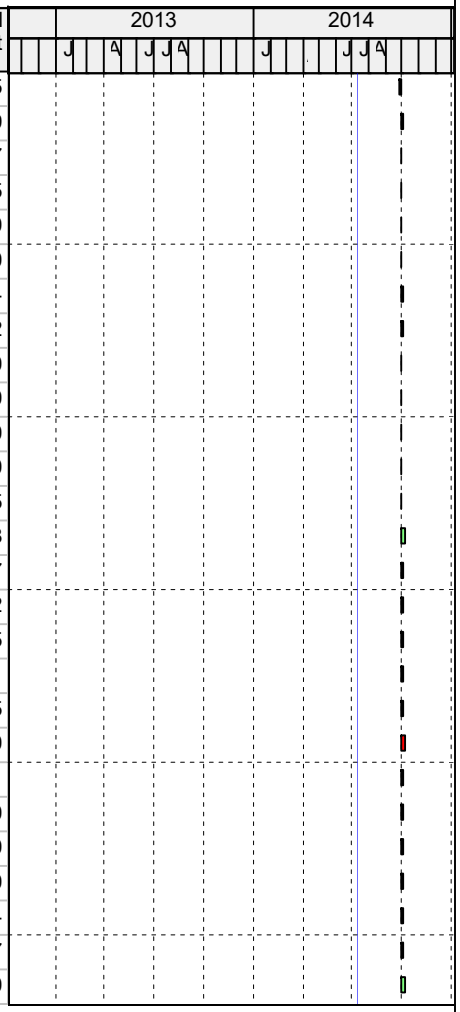



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8201 | Wall Finishes @ Corridors | 4 | 4 | 01-Oct-14 | 06-Oct-14 | 33 |
| LL1-Z5-8140 | Acoutical Ceiling Tile | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 41 |
| LL1-Z5-8126 | Doors & Hardware | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 39 |
| LL1-Z4-8132 | Contractor Pre-Punchlist | 3 | 3 | 02-Oct-14 | 06-Oct-14 | 45 |
| L1BOH1-8106 | Wallcoverings | 2 | 2 | 02-Oct-14 | 03-Oct-14 | 35 |
| L1BOH1-8201 | Final Coat Finish Paint | 2 | 2 | 02-Oct-14 | 03-Oct-14 | 35 |
| L1BOH2-8104 | Prime Paint | 2 | 2 | 02-Oct-14 | 03-Oct-14 | 17 |
| L1RR-8104 | Prime Paint | 2 | 2 | 02-Oct-14 | 03-Oct-14 | 15 |
| L14-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 34 |
| L15-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 27 |
| L16-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 21 |
| L17-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 20 |
| LL2E-8340 | LL2 - Install walk-in cooler/freezer (BY OTHERS) | 5 | 5 | 02-Oct-14 | 08-Oct-14 | 17 |
| L16-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 21 |
| L17-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 20 |
| LL1-Z3-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 02-Oct-14* | 03-Oct-14 | 42 |
| LL1-Z6-8124 | Flooring | 2 | 2 | 03-Oct-14 | 06-Oct-14 | 27 |
| LL1-Z5-8106 | Wallcoverings | 2 | 2 | 03-Oct-14 | 06-Oct-14 | 39 |
| LL1-Z5-8201 | Final Coat Finish Paint | 2 | 2 | 03-Oct-14 | 06-Oct-14 | 39 |
| L14-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 03-Oct-14 | 06-Oct-14 | 34 |
| L15-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 03-Oct-14 | 06-Oct-14 | 27 |
| L16-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 21 |
| L17-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 20 |
| L16-8405 | Cover Inspection | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 21 |
| L17-8405 | Cover Inspection | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 20 |
| L16-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 8 |
| LL1-Z7-8114 | T Bar Grid Ceiling | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 22 |

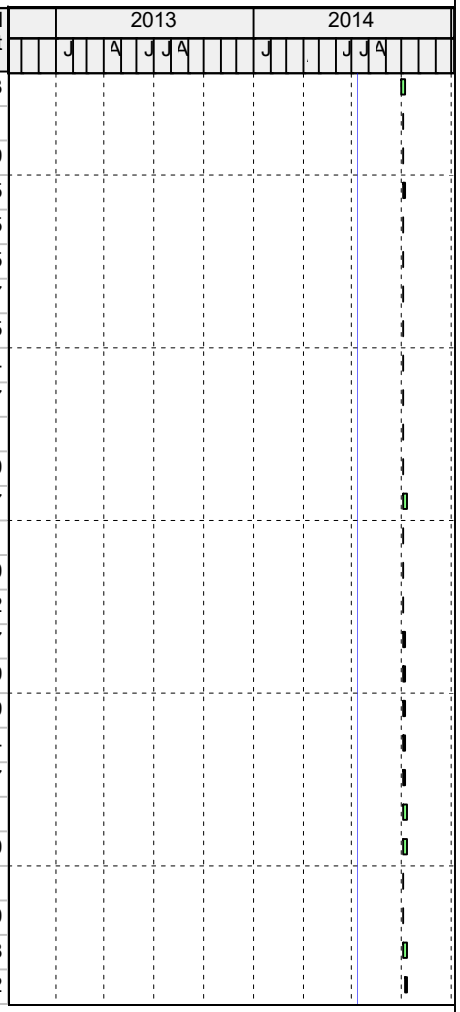



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1BOH1-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 39 |
| L1BOH1-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 37 |
| L1BOH1-8204 | Mech Trim / Finish (HVAC) | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 35 |
| L1BOH2-8114 | T Bar Grid Ceiling | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 17 |
| L1RR-8114 | T Bar Grid Ceiling | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 15 |
| LL1-Z5-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 39 |
| LL1-Z5-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 39 |
| LL1-Z5-8204 | Mech Trim / Finish (HVAC & Plumbing) | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 39 |
| LL1-Z6-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 1 | 1 | 07-Oct-14 | 07-Oct-14 | 38 |
| LL1-Z6-8126 | Doors & Hardware | 1 | 1 | 07-Oct-14 | 07-Oct-14 | 27 |
| LL1-Z4-8208 | Final Clean | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 45 |
| L14-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 07-Oct-14 | 07-Oct-14 | 34 |
| L15-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 07-Oct-14 | 07-Oct-14 | 27 |
| LL1-Z3-8140a | Acoustical Ceiling Tile (remainder) | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 39 |
| LL1-Z5-8203 | Install mirrors (by others) | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 39 |
| L15-8201 | Wall Finishes @ Corridors | 4 | 4 | 07-Oct-14 | 10-Oct-14 | 29 |
| LL1-Z6-8106 | Wallcoverings | 2 | 2 | 08-Oct-14 | 09-Oct-14 | 27 |
| LL1-Z6-8201 | Final Coat Finish Paint | 2 | 2 | 08-Oct-14 | 09-Oct-14 | 27 |
| L14-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 34 |
| L14-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 34 |
| L15-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 27 |
| L15-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 27 |
| LL1-Z7-8116 | Finish Carpentry / Millwork | 3 | 3 | 09-Oct-14 | 13-Oct-14 | 22 |
| LL1-Z5-8134 | Pre-Clean | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 39 |
| LL1-Z4-8210 | Owner Walk / Create Punchlist | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 45 |
| L1BOH2-8116 | Finish Carpentry / Millwork | 3 | 3 | 09-Oct-14 | 13-Oct-14 | 17 |
| L1RR-8116 | Finish Carpentry / Millwork | 4 | 4 | 09-Oct-14 | 14-Oct-14 | 14 |

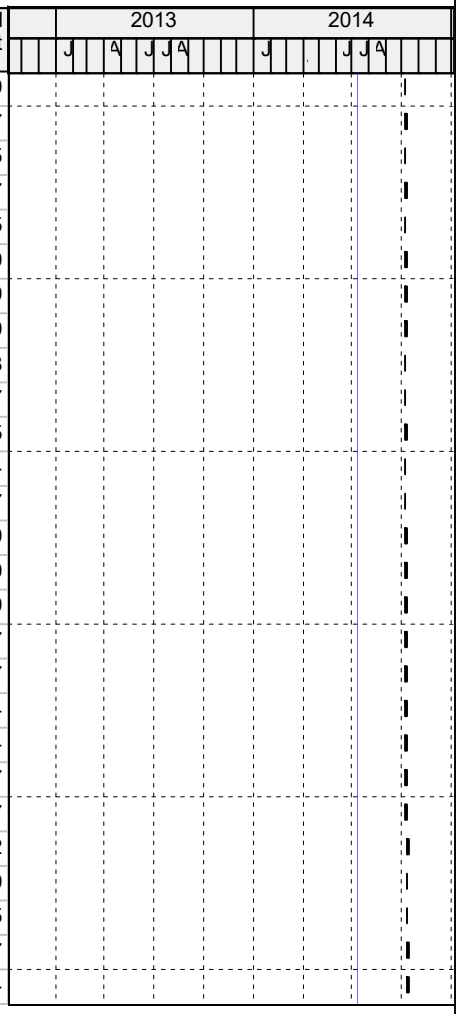



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8418 | Flooring at Elevator Lobby | 2 | 2 | 09-Oct-14 | 10-Oct-14 | 34 |
| L15-8418 | Flooring at Elevator Lobby | 2 | 2 | 09-Oct-14 | 10-Oct-14 | 34 |
| L16-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 21 |
| L17-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 20 |
| LL2E-8342 | LL2 - Final connections at walk-in cooler/freezer | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 38 |
| L1BOH1-8140a | Acoustical Ceiling Tile (remainder) | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 37 |
| L1L-8120 | Install plumbing at bar | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 9 |
| L1L-8122 | Install electrical at bar | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 9 |
| L1K-8340 | Install walk-in cooler/freezer (BY OTHERS0 | 10 | 10 | 09-Oct-14 | 22-Oct-14 | 17 |
| LL1-Z6-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 10-Oct-14 | 13-Oct-14 | 36 |
| LL1-Z6-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 10-Oct-14 | 13-Oct-14 | 35 |
| LL1-Z6-8204 | Mech Trim / Finish (HVAC & Plumbing) | 10 | 10 | 10-Oct-14 | 23-Oct-14 | 27 |
| LL1-Z4-8212 | Resolve Final Punchlist | 3 | 3 | 10-Oct-14 | 14-Oct-14 | 45 |
| LL1-Z5-8132 | Contractor Pre-Punchlist | 3 | 3 | 10-Oct-14 | 14-Oct-14 | 39 |
| L1BOH1-8134 | Pre-Clean | 2 | 2 | 10-Oct-14 | 13-Oct-14 | 37 |
| L16-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 21 |
| L17-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 20 |
| LL1-Z5-8136 | Install excercise equipment (by others) | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 43 |
| L16-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 13-Oct-14 | 14-Oct-14 | 21 |
| L17-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 13-Oct-14 | 14-Oct-14 | 20 |
| L16-8201 | Wall Finishes @ Corridors | 4 | 4 | 13-Oct-14 | 16-Oct-14 | 25 |
| L17-8129 | Install Shower Doors | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 0 |
| LL1-Z7-8200 | First Coat Finish Paint | 3 | 3 | 14-Oct-14 | 16-Oct-14 | 22 |
| L1BOH1-8132 | Contractor Pre-Punchlist | 3 | 3 | 14-Oct-14 | 16-Oct-14 | 37 |
| L1BOH2-8200 | First Coat Finish Paint | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 17 |
| LL1-Z4-8214 | LL1 Elevator Lobby / Lobby Complete | 0 | 0 |  | 14-Oct-14 | 45 |
| LL1-Z5-8208 | Final Clean | 2 | 2 | 15-Oct-14 | 16-Oct-14 | 39 |

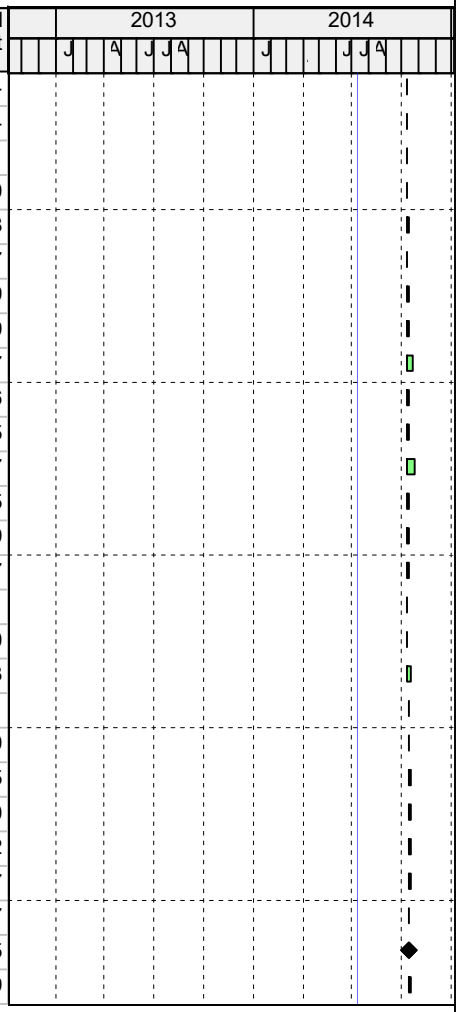



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1RR-8200 | First Coat Finish Paint | 2 | 2 | 15-Oct-14 | 16-Oct-14 | 14 |
| L16-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 15-Oct-14 | 15-Oct-14 | 21 |
| L17-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 15-Oct-14 | 15-Oct-14 | 20 |
| L1BOH2-8124 | Flooring | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 17 |
| L16-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 16-Oct-14 | 16-Oct-14 | 21 |
| L16-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 16-Oct-14 | 16-Oct-14 | 21 |
| L17-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 16-Oct-14 | 16-Oct-14 | 20 |
| L17-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 16-Oct-14 | 16-Oct-14 | 21 |
| L17-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 0 |
| LL1-Z7-8124 | Flooring | 3 | 3 | 17-Oct-14 | 21-Oct-14 | 22 |
| LL1-Z5-8210 | Owner Walk / Create Punchlist | 1 | 1 | 17-Oct-14 | 17-Oct-14 | 39 |
| L1BOH1-8208 | Final Clean | 2 | 2 | 17-Oct-14 | 20-Oct-14 | 37 |
| L1RR-8124 | Flooring | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 14 |
| L16-8418 | Flooring at Elevator Lobby | 2 | 2 | 17-Oct-14 | 20-Oct-14 | 28 |
| L17-8418 | Flooring at Elevator Lobby | 2 | 2 | 17-Oct-14 | 20-Oct-14 | 28 |
| LL1-Z5-8212 | Resolve Final Punchlist | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 39 |
| L1BOH1-8210 | Owner Walk / Create Punchlist | 1 | 1 | 21-Oct-14 | 21-Oct-14 | 37 |
| LL1-8140a | Acoustical Ceiling Tile (remainder) | 5 | 5 | 21-Oct-14 | 27-Oct-14 | 21 |
| LL1-Z7-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 1 | 1 | 22-Oct-14 | 22-Oct-14 | 26 |
| LL1-Z7-8126 | Doors & Hardware | 1 | 1 | 22-Oct-14 | 22-Oct-14 | 22 |
| L1BOH1-8212 | Resolve Final Punchlist | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 37 |
| LL1-Z5-8214 | LL1 Exercise Room Complete | 0 | 0 | | 22-Oct-14 | 39 |
| LL1-Z7-8106 | Wallcoverings | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 23 |
| LL1-Z7-8201 | Final Coat Finish Paint | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 22 |
| L1BOH2-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 24 |
| L1BOH2-8126 | Doors & Hardware | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 17 |
| I-1204 | Concierge Lounge - Additional millwork | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 5 |

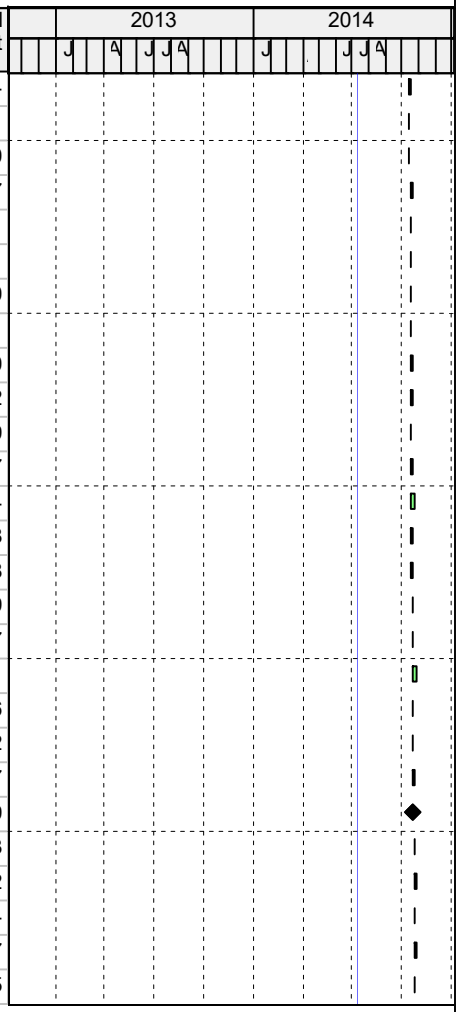



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8342 | Final connections at walk-in cooler/freezer | 10 | 10 | 23-Oct-14 | 05-Nov-14 | 17 |
| L1RR-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 2 | 2 | 24-Oct-14 | 27-Oct-14 | 23 |
| L1RR-8126 | Doors & Hardware | 2 | 2 | 24-Oct-14 | 27-Oct-14 | 14 |
| LL1-Z2-8118a | Install decorative light fixtures | 3 | 3 | 24-Oct-14 | 28-Oct-14 | 20 |
| LL1-Z6-8140a | Acoustical Ceiling Tile (remainder) | 1 | 1 | 24-Oct-14 | 24-Oct-14 | 27 |
| L17-8201 | Wall Finishes @ Corridors | 4 | 4 | 24-Oct-14 | 29-Oct-14 | 16 |
| L1BOH1-8214 | L1 East Service Corridor Complete | 0 | 0 | | 24-Oct-14 | 37 |
| LL1-Z6-8134 | Pre-Clean | 1 | 1 | 27-Oct-14 | 27-Oct-14 | 27 |
| L1B-8140a | Acoustical Ceiling Tile (remainder) | 3 | 3 | 27-Oct-14 | 29-Oct-14 | 21 |
| LL1-Z7-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 28-Oct-14 | 30-Oct-14 | 23 |
| LL1-Z7-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 28-Oct-14 | 30-Oct-14 | 22 |
| LL1-Z7-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 28-Oct-14 | 30-Oct-14 | 22 |
| LL1-Z6-8132 | Contractor Pre-Punchlist | 3 | 3 | 28-Oct-14 | 30-Oct-14 | 27 |
| L1BOH2-8106 | Wallcoverings | 2 | 2 | 28-Oct-14 | 29-Oct-14 | 17 |
| L1BOH2-8201 | Final Coat Finish Paint | 2 | 2 | 28-Oct-14 | 29-Oct-14 | 17 |
| L1RR-8106 | Wall Coverings | 2 | 2 | 28-Oct-14 | 29-Oct-14 | 14 |
| L1RR-8201 | Final Coat Finish Paint | 1 | 1 | 28-Oct-14 | 28-Oct-14 | 15 |
| L1BOH2-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 21 |
| L1BOH2-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 20 |
| L1BOH2-8204 | Mech Trim / Finish (HVAC & Plumbing) | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 17 |
| L1RR-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 21 |
| L1RR-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 20 |
| L1RR-8204 | Mech Trim / Finish (HVAC & Plumbing) | 5 | 5 | 30-Oct-14 | 05-Nov-14 | 14 |
| LL1-Z6-8208 | Final Clean | 2 | 2 | 31-Oct-14 | 03-Nov-14 | 27 |
| LL1-Z2-8140a | Acoustical Ceiling Tile (remainder) | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 15 |
| LL1-Z7-8140a | Acoustical Ceiling Tile (remainder) | 1 | 1 | 31-Oct-14 | 31-Oct-14 | 22 |
| L1K-8128 | Install Kitchen equipment (BY OTHERS) | 10 | 10 | 31-Oct-14 | 14-Nov-14 | 11 |

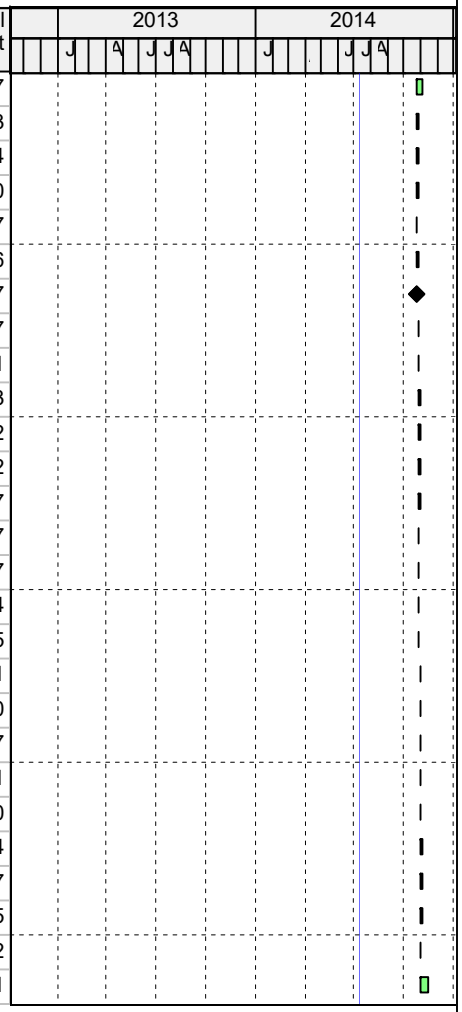



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z7-8134 | Pre-Clean | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 22 |
| L1BOH2-8140a | Acoustical Ceiling Tile (remainder) | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 20 |
| LL1-Z6-8210 | Owner Walk / Create Punchlist | 1 | 1 | 04-Nov-14 | 04-Nov-14 | 27 |
| LL1-Z7-8132 | Contractor Pre-Punchlist | 3 | 3 | 04-Nov-14 | 06-Nov-14 | 22 |
| L1BOH2-8134 | Pre-Clean | 2 | 2 | 04-Nov-14 | 05-Nov-14 | 20 |
| I-1202 | Concierge Lounge - Additional flooring work | 1 | 1 | 04-Nov-14 | 04-Nov-14 | 4 |
| CO-7100T | CO - Preliminary Start-Up & Testing (Tower) | 10 | 10 | 04-Nov-14 | 18-Nov-14 | 0 |
| LL1-Z6-8212 | Resolve Final Punchlist | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 27 |
| L1BOH2-8132 | Contractor Pre-Punchlist | 3 | 3 | 06-Nov-14 | 11-Nov-14 | 20 |
| L1RR-8140a | Acoustical Ceiling Tile (remainder) | 1 | 1 | 06-Nov-14 | 06-Nov-14 | 17 |
| LL1-Z7-8208 | Final Clean | 2 | 2 | 07-Nov-14 | 11-Nov-14 | 22 |
| L1RR-8134 | Pre-Clean | 2 | 2 | 07-Nov-14 | 11-Nov-14 | 17 |
| I-1602 | Enclosure at manlift - Framing & windows | 6 | 6 | 07-Nov-14 | 17-Nov-14 | 17 |
| LL1-Z6-8214 | LL1 - Public Restroom Complete | 0 | 0 | | 07-Nov-14 | 27 |
| LL1-Z7-8210 | Owner Walk / Create Punchlist | 1 | 1 | 12-Nov-14 | 12-Nov-14 | 22 |
| L1BOH2-8208 | Final Clean | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 20 |
| L1RR-8132 | Contrator Pre-Punchlist | 3 | 3 | 12-Nov-14 | 14-Nov-14 | 17 |
| LL1-Z7-8212 | Resolve Final Punchlist | 3 | 3 | 13-Nov-14 | 17-Nov-14 | 22 |
| I-1604 | Enclosure at manlift - GWB | 6 | 6 | 13-Nov-14 | 20-Nov-14 | 17 |
| L1BOH2-8210 | Owner Walk / Create Punchlist | 1 | 1 | 14-Nov-14 | 14-Nov-14 | 20 |
| L1BOH2-8212 | Resolve Final Punchlist | 3 | 3 | 17-Nov-14 | 19-Nov-14 | 20 |
| L1RR-8208 | Final Clean | 2 | 2 | 17-Nov-14 | 18-Nov-14 | 17 |
| I-1606 | Enclosure at manlift - Paint & finishes | 4 | 4 | 17-Nov-14 | 20-Nov-14 | 17 |
| I-1608 | Enclosure at manlift - Metal panels | 6 | 6 | 17-Nov-14 | 24-Nov-14 | 17 |
| L1K-8140a | Acoustical Ceiling Tile (remainder) | 3 | 3 | 17-Nov-14 | 19-Nov-14 | 8 |
| LL1-Z7-8214 | LL1 Back of House Complete | 0 | 0 | | 17-Nov-14 | 22 |
| L1RR-8210 | Owner Walk / Create Punchlist | 1 | 1 | 19-Nov-14 | 19-Nov-14 | 17 |

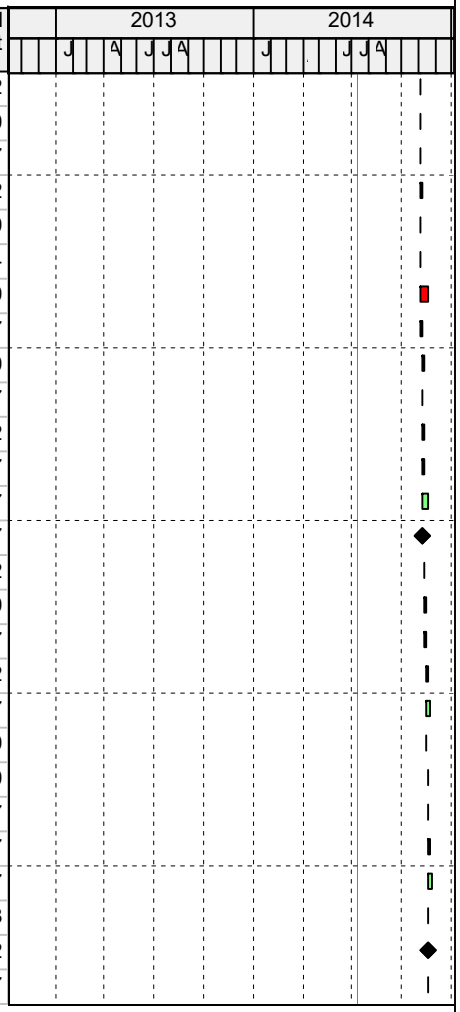



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7102T | CO - HVAC Commissioning (Tower) | 5 | 5 | 19-Nov-14 | 25-Nov-14 | 16 |
| CO-7110T | Fire Sprinkler Pre-Testing (Tower) | 5 | 5 | 19-Nov-14 | 25-Nov-14 | 11 |
| CO-7116T | Fire Alarm Pre-Testing (Tower) | 5 | 5 | 19-Nov-14 | 25-Nov-14 | 11 |
| CO-7104T | Smoke Control Pre-Testing (Tower) | 5 | 5 | 19-Nov-14 | 25-Nov-14 | 11 |
| L1BOH2-81214 | L1 Back of House Complete | 0 | 0 | | 19-Nov-14 | 20 |
| L1RR-8212 | Resolve Final Punchlist | 3 | 3 | 20-Nov-14 | 24-Nov-14 | 17 |
| L1RR-8214 | L1 Public Restroom Complete | 0 | 0 | | 24-Nov-14 | 17 |
| CO-7112T | City of Bellevue Fire Sprinkler Inspection / Approval (T | 5 | 5 | 26-Nov-14 | 04-Dec-14 | 11 |
| CO-7118T | City of Bellevue Fire Alarm Inspection / Approval (Tow | 5 | 5 | 26-Nov-14 | 04-Dec-14 | 11 |
| CO-7106T | City of Bellevue Smoke Control Testing (Tower) | 5 | 5 | 26-Nov-14 | 04-Dec-14 | 11 |
| CO-7124 | Complete Final Building Inspections | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 4 |
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13 A | | |
| CM-1002 | CM - Contract Time (578 Cal Days) | 576 | 86 | 06-Mar-13 A | 05-Oct-14 | 86 |
| CM-1014 | CM - Start of Construction | 0 | 0 | 05-Apr-13 A | | |
| CM-1006 | Construction Documents Issued by Client - (Due on 7 | 0 | 0 | 12-Jul-14 | | 172 |
| CM-1008 | Finalization of Allowances - (Due on 9-2-13) | 0 | 0 | 12-Jul-14 | | 172 |
| CO-7004 | CO - Prep / Submit O&M Manuals | 40 | 40 | 16-Oct-14 | 24-Nov-14 | 36 |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 19-Nov-14 | | 0 |
| CM-1016 | CM - Owner FF+E "Build-Out" | 42 | 42 | 19-Nov-14 | 30-Dec-14 | 0 |
| CM-1018 | CM - Hotel Operations Training | 21 | 21 | 04-Dec-14* | 24-Dec-14 | 6 |
| CO-7122 | CO - Certificate of Occupancy | 0 | 0 | | 22-Dec-14 | 8 |
| CO-7006 | CO - Certificate of Occupancy/Substantial Completior | 0 | 0 | | 30-Dec-14 | 0 |
| **Misc Milestones** | | | | | | |

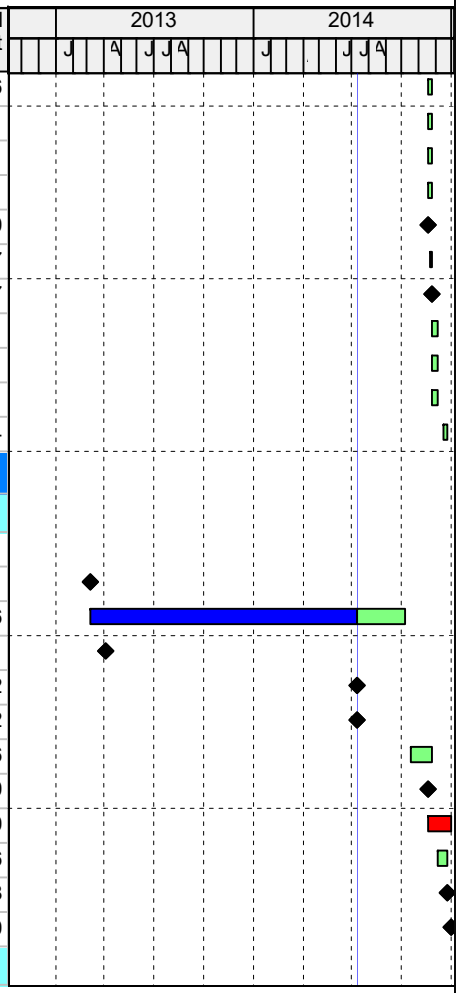



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CM-1020 | MM - Site Mobilization | 10 | 0 | 06-Mar-13 A | 04-Apr-13 A | |
| MM-1008 | MM - Top Out - Tower / Structure | 0 | 0 | | 16-Apr-14 A | |
| MM-1004 | MM - Start Drywall In Tower | 0 | 0 | 27-Jun-14 A | | |
| MM-1010 | Energize Permanent Power | 5 | 5 | 01-Aug-14 | 05-Aug-14 | 117 |
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 13-Aug-14 | 86 |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| Tower Crane | | | | | | |
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 0 | 04-Jun-13 A | 14-Jun-13 A | |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 0 | 20-Jun-13 A | 24-Jun-13 A | |
| TC-5902 | Tower Crane - Erectiion | 2 | 0 | 21-Jun-13 A | 24-Jun-13 A | |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 24-Jun-13 A | | |
| TC-5906 | Tower Crane - Operatational Period | 391 | 0 | 24-Jun-13 A | 16-Jun-14 A | |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 0 | 16-Jun-14 A | 17-Jun-14 A | |
| Man & Material Lifts | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 0 | 14-Jan-14 A | 20-Jan-14 A | |
| ML-5952 | Man/Material Lifts - Erect/Build Loading Dock | 5 | 0 | 21-Jan-14 A | 27-Jan-14 A | |
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 10-Feb-14 A | | |
| ML-5954 | Man/Material Lifts - Load Test / Certify | 1 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| ML-5958 | Man/Material Lifts - Operatational Period | 196 | 111 | 10-Feb-14 A | 30-Oct-14 | 26 |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 5 | 5 | 31-Oct-14 | 06-Nov-14 | 17 |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |
| Mass Excavation / Shoring | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 0 | 05-Apr-13 A | 12-Apr-13 A | |
| SW-2002 | Demolition And Utility Relocation | 8 | 0 | 15-Apr-13 A | 19-Apr-13 A | |
| SW-2010 | Grade Subgrade for Elect/Plumbing | 3 | 0 | 07-Jan-14 A | 09-Jan-14 A | |

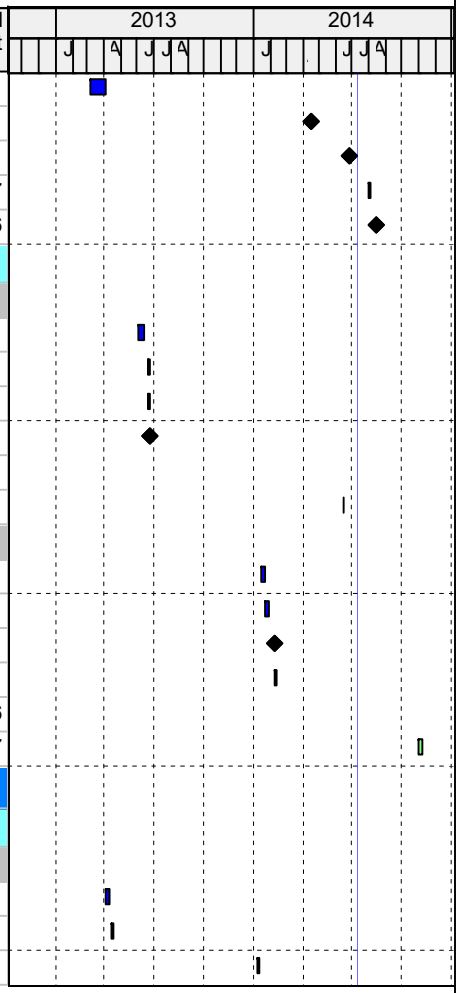



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Site Finishes** | | | | | | |
| SW-2006 | Install Perm Power Electrical Service / Dry Utilities (Offi | 15 | 0 | 20-May-14 A | 05-Jun-14 A | |
| SW-2004 | Offsite Water & Water Connection | 5 | 5 | 21-Jul-14 | 25-Jul-14 | 83 |
| SW-2008 | Sidewalks / Landscaping / Street Improvements | 40 | 40 | 29-Aug-14 | 24-Oct-14 | 30 |
| **Structure** | | | | | | |
| **Foundation / Substructure - (Levels LL4 / LL3)** | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 0 | 12-Jun-13 A | 27-Jun-13 A | |
| LL4-1601 | LL4 - Excavate Footings | 14 | 0 | 17-Jun-13 A | 30-Jul-13 A | |
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 0 | 18-Jun-13 A | 24-Jun-13 A | |
| LL4-1606 | LL4 - Undrgmd Plumbing | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-1608 | LL4 - Undrgmd Elec | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 0 | 19-Jun-13 A | 25-Jun-13 A | |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 0 | 26-Jun-13 A | 02-Aug-13 A | |
| LL4-2033 | LL4 - Shotcrete Walls | 27 | 0 | 26-Jun-13 A | 05-Aug-13 A | |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 0 | 03-Jul-13 A | 21-Aug-13 A | |
| LL4-1614 | LL4 - FRP SOG | 5 | 0 | 10-Jul-13 A | 07-Aug-13 A | |
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 0 | 12-Jul-13 A | 26-Jul-13 A | |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 0 | 13-Jul-13 A | 06-Aug-13 A | |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 0 | 22-Jul-13 A | 24-Jul-13 A | |
| LL4-1618 | LL4 - FRP Ramp SOG | 5 | 0 | 01-Aug-13 A | 07-Aug-13 A | |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2004 | LL2 - Shore / Form Deck | 8 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2006 | LL3 - M & E Inserts | 4 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2008 | LL3 - ReSteel / PT Cables | 6 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2010 | LL3 - Install Embeds | 2 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2001 | LL3 - Waterproof Walls | 3 | 0 | 05-Aug-13 A | 05-Aug-13 A | |

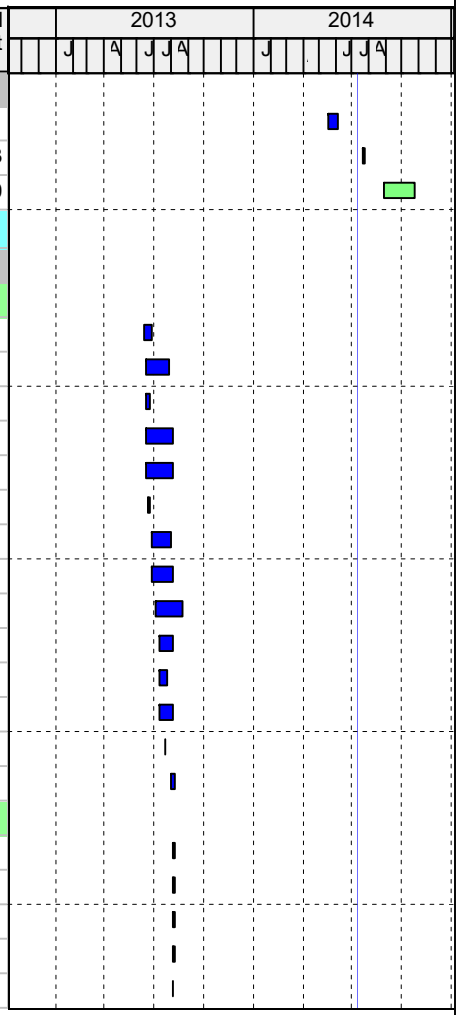



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-2012 | LL3 - Pour / Finish Deck | 2 | 0 | 16-Aug-13 A | 16-Aug-13 A | |
| LL3-2014 | LL3 - Stress Tendons | 1 | 0 | 19-Aug-13 A | 19-Aug-13 A | |
| LL3-2000 | LL3 - FRP Core Walls | 8 | 0 | 19-Aug-13 A | 28-Aug-13 A | |
| LL3-2033 | LL3 - Shotcrete Walls | 5 | 0 | 23-Aug-13 A | 26-Aug-13 A | |
| LL3-2016 | LL3 - Strip / ReShore Deck | 3 | 0 | 01-Sep-13 A | 13-Sep-13 A | |
| LL3-2018 | LL3 - Remove ReShores | 4 | 0 | 04-Nov-13 A | 07-Nov-13 A | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Grids 1 to 4 - (SOG @ Loading Dock)** | | | | | | |
| LL2-2056 | LL2 - Grease Intercepter | 5 | 0 | 15-Aug-13 A | 21-Aug-13 A | |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 0 | 27-Aug-13 A | 04-Sep-13 A | |
| LL2-2027 | LL2 - Waterproof Walls | 2 | 0 | 27-Aug-13 A | 28-Aug-13 A | |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 0 | 30-Aug-13 A | 05-Sep-13 A | |
| LL2-2021 | LL2 - FRP Elec Vault | 14 | 0 | 30-Aug-13 A | 04-Sep-13 A | |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 0 | 04-Sep-13 A | 11-Sep-13 A | |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 0 | 11-Sep-13 A | 13-Sep-13 A | |
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls/Roof | 11 | 0 | 19-Sep-13 A | 03-Oct-13 A | |
| LL2-2020 | LL2 - Undrgmd Plumbing | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2022 | LL2 - Undrgmd Elec | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2031 | LL2 - FRP Generator SOG | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2015 | LL2 to LL1 FRP Columns / Misc Walls | 6 | 0 | 01-Oct-13 A | 01-Oct-13 A | |
| LL2-2029 | LL2 - F/R/P Pour #2 | 8 | 0 | 15-Jan-14 A | 24-Jan-14 A | |
| LL2-2011 | LL2 - F/R/P Pour #3 | 16 | 0 | 24-Jan-14 A | 18-Feb-14 A | |
| LL2-2019 | LL2 - F/R/P Pour #6 | 4 | 0 | 19-Feb-14 A | 17-Mar-14 A | |
| LL2-2044 | LL2 - Set Generator | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |

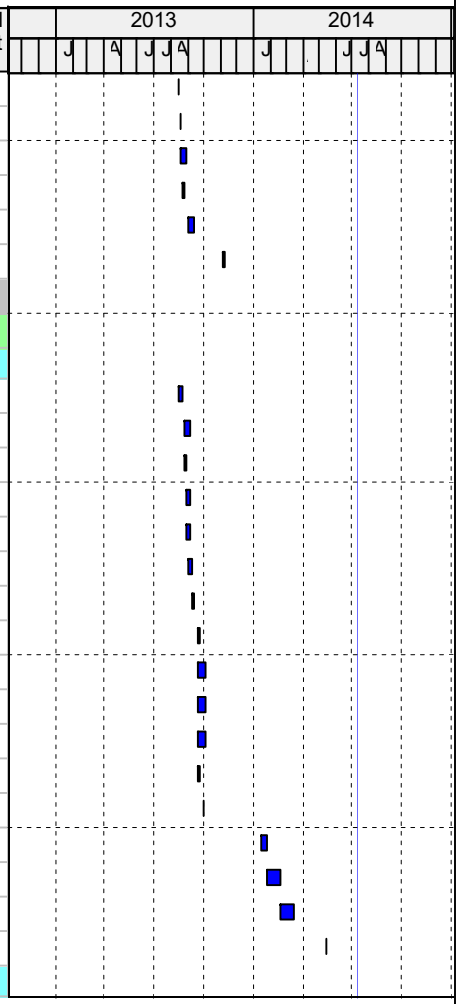



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2004 | LL2 - Shore / Form Deck | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2035 | LL2 to LL1 - Shotcrete Walls | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2006 | LL2 - M & E Inserts | 4 | 0 | 14-Aug-13 A | 19-Aug-13 A | |
| LL2-2008 | LL2 - ReSteel / PT Cables | 6 | 0 | 14-Aug-13 A | 21-Aug-13 A | |
| LL2-2010 | LL2 - Install Embeds | 3 | 0 | 14-Aug-13 A | 16-Aug-13 A | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 0 | 27-Aug-13 A | 06-Sep-13 A | |
| LL2-2012 | LL2 - Place / Finish Deck | 3 | 0 | 29-Aug-13 A | 29-Aug-13 A | |
| LL2-2023 | LL2 - Waterproof Walls | 3 | 0 | 29-Aug-13 A | 03-Sep-13 A | |
| LL2-2014 | LL2 - Stress Tendons | 1 | 0 | 30-Aug-13 A | 30-Aug-13 A | |
| LL2-2016 | LL2 - Strip / ReShore | 3 | 0 | 03-Sep-13 A | 05-Sep-13 A | |
| LL2-8234 | LL2 - Place / Finish Deck | 3 | 0 | 12-Sep-13 A | 12-Sep-13 A | |
| LL2-2000 | LL2 - FRP Core Walls | 8 | 0 | 12-Sep-13 A | 23-Sep-13 A | |
| LL2-2018 | LL2 - Remove ReShores | 4 | 0 | 13-Nov-13 A | 18-Nov-13 A | |
| LL2-2013 | LL2 - F/R/P Pour #1 | 4 | 0 | 13-Jan-14 A | 16-Jan-14 A | |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| P5A-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2000 | LL1 - FRP Core Walls | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2004 | LL1 - Shore / Form Deck | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| P6-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P6-2004 | LL1 - Shore / Form Deck | 7 | 0 | 16-Sep-13 A | 24-Sep-13 A | |
| P5A-2006 | LL1 - MEP Rough In | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2008 | LL1 - ReSteel / PT Cables | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2012 | LL1 - Place / Finish Deck | 0 | 0 | 20-Sep-13 A | | |
| P5A-2020 | LL1 - Waterproof Walls | 3 | 0 | 20-Sep-13 A | 24-Sep-13 A | |
| P5A-2014 | LL1 - Stress Tendons | 1 | 0 | 23-Sep-13 A | 23-Sep-13 A | |
| P5A-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |

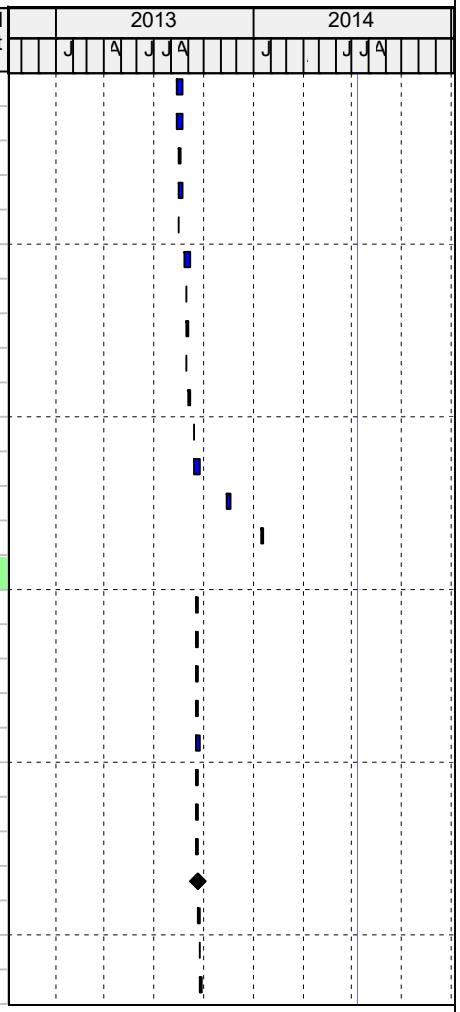



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P6-2006 | LL1 - MEP Rough In | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2008 | LL1 - ReSteel / PT Cables | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 24-Sep-13 A | 25-Sep-13 A | |
| P6-2020 | LL1 - Waterproof Walls | 4 | 0 | 24-Sep-13 A | 27-Sep-13 A | |
| P5A-2033 | LL1 - Resteel/Shotcrete Walls | 3 | 0 | 25-Sep-13 A | 27-Sep-13 A | |
| P5B-2002 | LL1 - FRP Columns Below | 5 | 0 | 26-Sep-13 A | 02-Oct-13 A | |
| P5B-2004 | LL1 - Shore / Form Deck | 7 | 0 | 26-Sep-13 A | 04-Oct-13 A | |
| P6-2012 | LL1 - Place / Finish Deck | 0 | 0 | 27-Sep-13 A | | |
| P6-2014 | LL1 - Stress Tendons | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2033 | LL1 - Resteel/Shotcrete Walls | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 01-Oct-13 A | 03-Oct-13 A | |
| P5B-2006 | LL1 - MEP Rough In | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2002 | FRP Columns Below | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2004 | Shore / Form Deck | 4 | 0 | 03-Oct-13 A | 08-Oct-13 A | |
| P5B-2008 | LL1 - ReSteel / PT Cables | 5 | 0 | 04-Oct-13 A | 10-Oct-13 A | |
| P5B-2010 | LL1 - Install Edgeform/Embeds | 4 | 0 | 04-Oct-13 A | 09-Oct-13 A | |
| P8-2002 | FRP Columns Below | 5 | 0 | 07-Oct-13 A | 11-Oct-13 A | |
| P8-2000 | Form/Resteel/Close Core Walls | 14 | 0 | 07-Oct-13 A | 24-Oct-13 A | |
| P8-2004 | Shore / Form Deck P8 | 8 | 0 | 07-Oct-13 A | 16-Oct-13 A | |
| P7-2002 | FRP Columns Below | 5 | 0 | 08-Oct-13 A | 14-Oct-13 A | |
| P7-2004 | Shore / Form Deck | 6 | 0 | 08-Oct-13 A | 15-Oct-13 A | |
| P10A--2006 | MEP Rough In | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2008 | ReSteel / PT Cables | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2010 | Install Edgeform/Embeds | 2 | 0 | 08-Oct-13 A | 09-Oct-13 A | |
| P5B-2012 | LL1 - Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P10A--2012 | Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P5B-2014 | LL1 - Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |

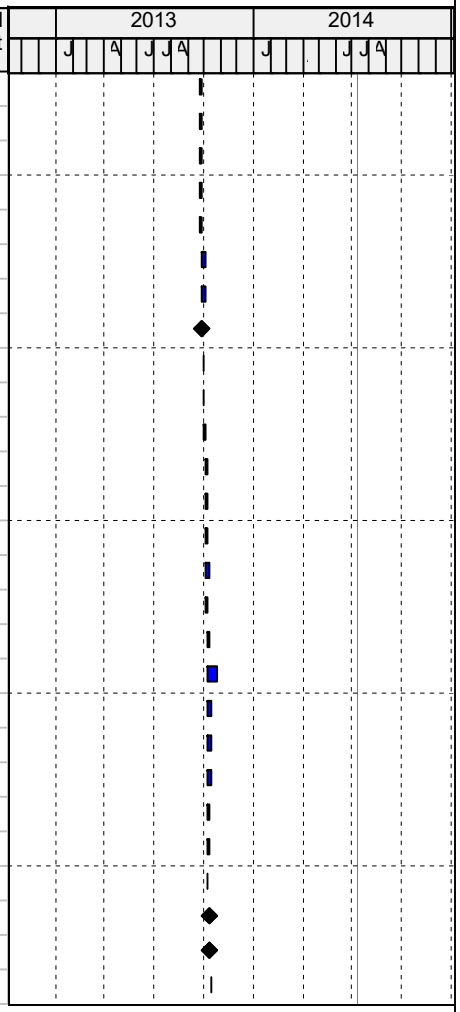



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P7-2006 | MEP Rough In | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P7-2008 | ReSteel / PT Cables | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P10A--2014 | Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P8-2020 | Shore / Form Deck P9 | 6 | 0 | 14-Oct-13 A | 21-Oct-13 A | |
| P5B-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2010 | Install Edgeform/Embeds | 2 | 0 | 15-Oct-13 A | 16-Oct-13 A | |
| P8-2006 | MEP Rough In | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2008 | ReSteel / PT Cables | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2010 | Install Edgeform/Embeds | 4 | 0 | 15-Oct-13 A | 18-Oct-13 A | |
| P10A--2016 | Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2012 | Place / Finish Deck | 0 | 0 | 18-Oct-13 A | | |
| P7-2033 | Resteel/Shotcrete Walls | 3 | 0 | 18-Oct-13 A | 22-Oct-13 A | |
| P7-2014 | Stress Tendons | 1 | 0 | 21-Oct-13 A | 21-Oct-13 A | |
| P7-2016 | Strip / ReShore Deck | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2002 | FRP Columns Below | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P10B--2000 | FRP Shear Walls Below | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2004 | Shore / Form Deck | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P8-2012 | Place / Finish Deck P 8 & 9 and Core Walls | 0 | 0 | 25-Oct-13 A | | |
| P8-2014 | Stress Tendons | 1 | 0 | 28-Oct-13 A | 28-Oct-13 A | |
| P10B--2006 | MEP Rough In | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2008 | ReSteel / PT Cables | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2010 | Install Edgeform/Embeds | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P12--2002 | FRP Columns Below | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P12--2000 | Form/Resteel/Close Core Walls | 9 | 0 | 28-Oct-13 A | 07-Nov-13 A | |
| P12--2004 | Shore / Form Deck | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P8-2016 | Strip / ReShore Deck | 3 | 0 | 29-Oct-13 A | 31-Oct-13 A | |
| P11--2002 | FRP Columns Below | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |

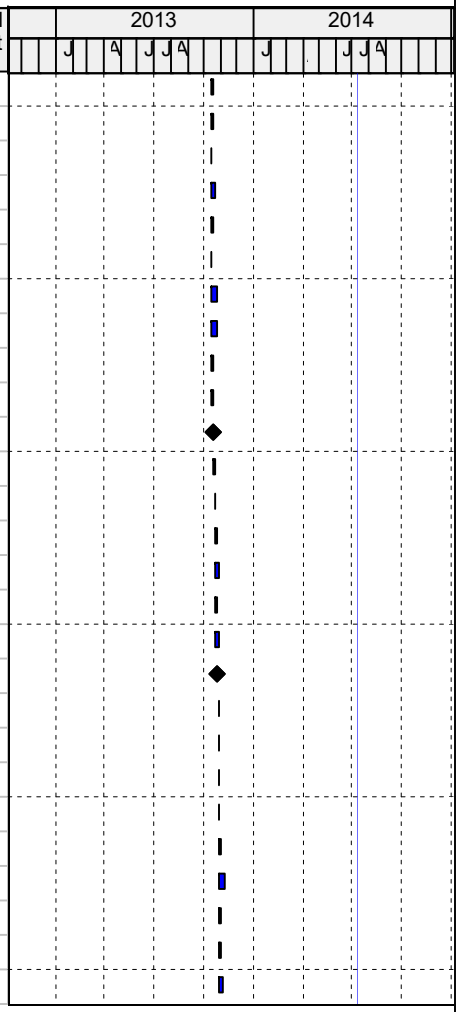



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P11–2004 | Shore / Form Deck | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P10B–2012 | Place / Finish Deck | 0 | 0 | 31-Oct-13 A | | |
| P10B–2014 | Stress Tendons | 1 | 0 | 01-Nov-13 A | 01-Nov-13 A | |
| P12–2006 | MEP Rough In | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12–2008 | ReSteel / PT Cables | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12–2010 | Install Edgeform/Embeds | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P10B–2016 | Strip / ReShore Deck | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2006 | MEP Rough In | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2008 | ReSteel / PT Cables | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2010 | Install Edgeform/Embeds | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2012 | Place / Finish Deck | 0 | 0 | 07-Nov-13 A | | |
| P13–2002 | FRP Columns Below | 5 | 0 | 07-Nov-13 A | 14-Nov-13 A | |
| P13–2004 | Shore / Form Deck | 9 | 0 | 07-Nov-13 A | 28-Nov-13 A | |
| P11–2014 | Stress Tendons | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| P12–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 08-Nov-13 A | | |
| P11–2016 | Strip / ReShore Deck | 3 | 0 | 12-Nov-13 A | 14-Nov-13 A | |
| P12–2014 | Stress Tendons | 1 | 0 | 12-Nov-13 A | 12-Nov-13 A | |
| P14–2002 | FRP Columns Below | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P14–2000 | Form/Resteel/Close Core Walls | 8 | 0 | 19-Nov-13 A | 03-Dec-13 A | |
| P14–2004 | Shore / Form Deck | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P13A–2002 | FRP Columns Below | 5 | 0 | 21-Nov-13 A | 27-Nov-13 A | |
| P13A–2004 | Shore / Form Deck | 4 | 0 | 21-Nov-13 A | 26-Nov-13 A | |
| P13–2010 | Install Edgeform/Embeds | 5 | 0 | 22-Nov-13 A | 04-Dec-13 A | |
| P13–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2006 | MEP Rough In | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2010 | Install Edgeform/Embeds | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |

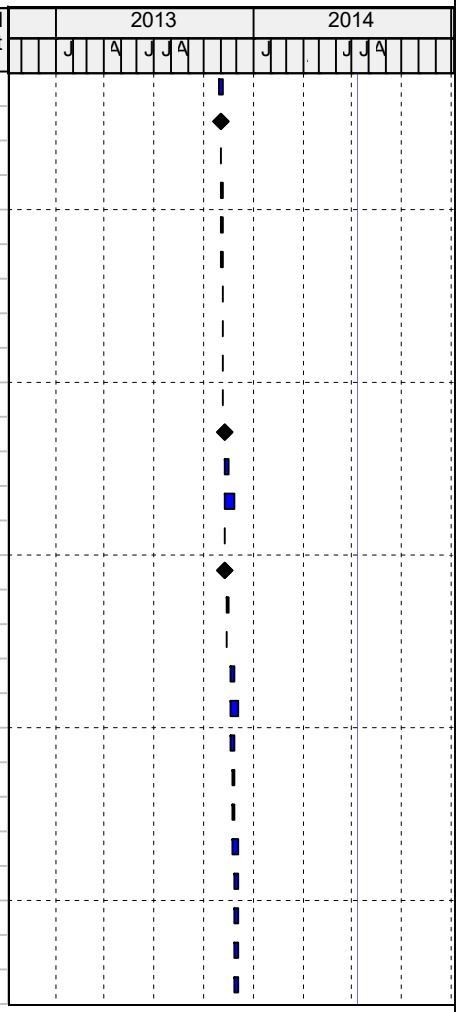



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P13–2006 | MEP Rough In | 5 | 0 | 26-Nov-13 A | 03-Dec-13 A | |
| P13A–2006 | MEP Rough In | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2008 | ReSteel / PT Cables | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2010 | Install Edgeform/Embeds | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13–2012 | Place / Finish Deck | 0 | 0 | 02-Dec-13 A | | |
| P13A–2012 | Place / Finish Deck | 0 | 0 | 03-Dec-13 A | | |
| P14–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 04-Dec-13 A | | |
| P13–2014 | Stress Tendons | 1 | 0 | 05-Dec-13 A | 05-Dec-13 A | |
| P15–2002 | FRP Columns Below | 3 | 0 | 05-Dec-13 A | 09-Dec-13 A | |
| P15–2000 | Jump/Resteel/Close Core | 9 | 0 | 05-Dec-13 A | 17-Dec-13 A | |
| P15–2004 | Shore / Form Deck | 5 | 0 | 05-Dec-13 A | 11-Dec-13 A | |
| P13–2016 | Strip / ReShore Deck | 3 | 0 | 06-Dec-13 A | 10-Dec-13 A | |
| P13A–2014 | Stress Tendons | 1 | 0 | 06-Dec-13 A | 06-Dec-13 A | |
| P14–2014 | Stress Tendons | 1 | 0 | 07-Dec-13 A | 07-Dec-13 A | |
| P15–2006 | MEP Rough In | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2008 | ReSteel / PT Cables | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2010 | Install Edgeform/Embeds | 3 | 0 | 11-Dec-13 A | 13-Dec-13 A | |
| P16-2002 | FRP Columns Below | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P16-2004 | Shore / Form Deck | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P15–2012 | Place / Finish Deck | 0 | 0 | 18-Dec-13 A | | |
| P15–2020 | Place Conc @ Core | 0 | 0 | 18-Dec-13 A | | |
| P16-2000 | Jump/Resteel/Close Core | 5 | 0 | 18-Dec-13 A | 24-Dec-13 A | |
| P16-2006 | MEP Rough In | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2008 | ReSteel / PT Cables | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2010 | Install Edgeform/Embeds | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P15–2014 | Stress Tendons | 1 | 0 | 21-Dec-13 A | 21-Dec-13 A | |
| P8-2018 | Remove Reshores | 2 | 0 | 23-Dec-13 A | 24-Dec-13 A | |

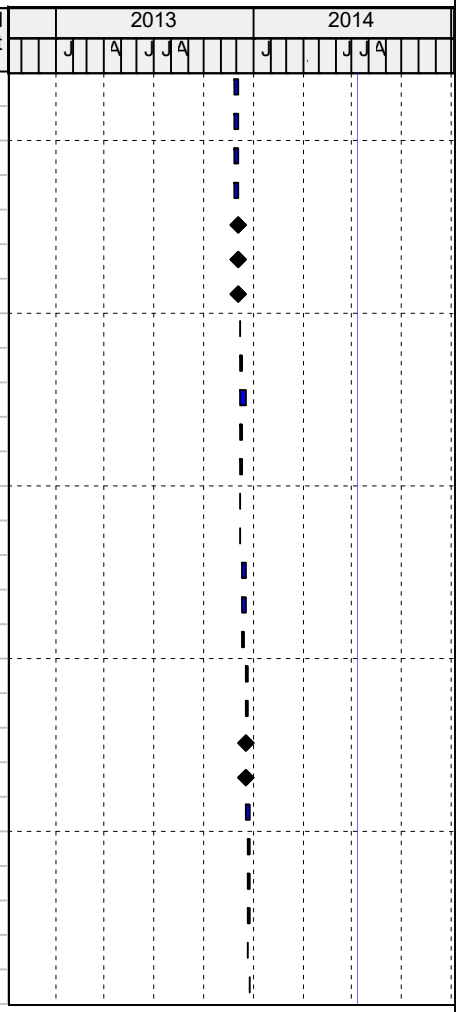



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P10A--2018 | Remove Reshores | 2 | 0 | 26-Dec-13 A | 27-Dec-13 A | |
| P16-2012 | Place / Finish Deck | 0 | 0 | 26-Dec-13 A | | |
| P16-2020 | Place Conc @ Core | 0 | 0 | 26-Dec-13 A | | |
| P17-2002 | FRP Columns Below | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P17-2000 | Jump/Resteel/Close Core | 7 | 0 | 27-Dec-13 A | 07-Jan-14 A | |
| P17-2004 | Shore / Form Deck | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P10B--2018 | Remove Reshores | 2 | 0 | 30-Dec-13 A | 31-Dec-13 A | |
| P16-2014 | Stress Tendons | 1 | 0 | 31-Dec-13 A | 31-Dec-13 A | |
| P5A-2018 | LL1 - Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P11--2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P12--2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P17-2006 | MEP Rough In | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2008 | ReSteel / PT Cables | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2010 | Install Edgeform/Embeds | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P6-2018 | LL1 - Remove Reshores | 2 | 0 | 06-Jan-14 A | 07-Jan-14 A | |
| P5B-2018 | LL1 - Remove Reshores | 2 | 0 | 08-Jan-14 A | 09-Jan-14 A | |
| P17-2012 | Place / Finish Deck | 0 | 0 | 08-Jan-14 A | | |
| P17-2020 | Place Conc @ Core | 0 | 0 | 08-Jan-14 A | | |
| P18-2002 | FRP Columns Below | 5 | 0 | 09-Jan-14 A | 15-Jan-14 A | |
| P18-2000 | Jump/Resteel/Close Core | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P18-2004 | Shore / Form Deck | 3 | 0 | 09-Jan-14 A | 13-Jan-14 A | |
| LL2-2022R | MEP Rough In | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P7-2018 | Remove Reshores | 2 | 0 | 10-Jan-14 A | 13-Jan-14 A | |
| P17-2014 | Stress Tendons | 1 | 0 | 11-Jan-14 A | 11-Jan-14 A | |
| P13--2018 | Remove Reshores | 2 | 0 | 13-Jan-14 A | 14-Jan-14 A | |
| P13A--2018 | Remove Reshores | 2 | 0 | 15-Jan-14 A | 16-Jan-14 A | |
| WEA-2012 | WIND IMPACT | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |

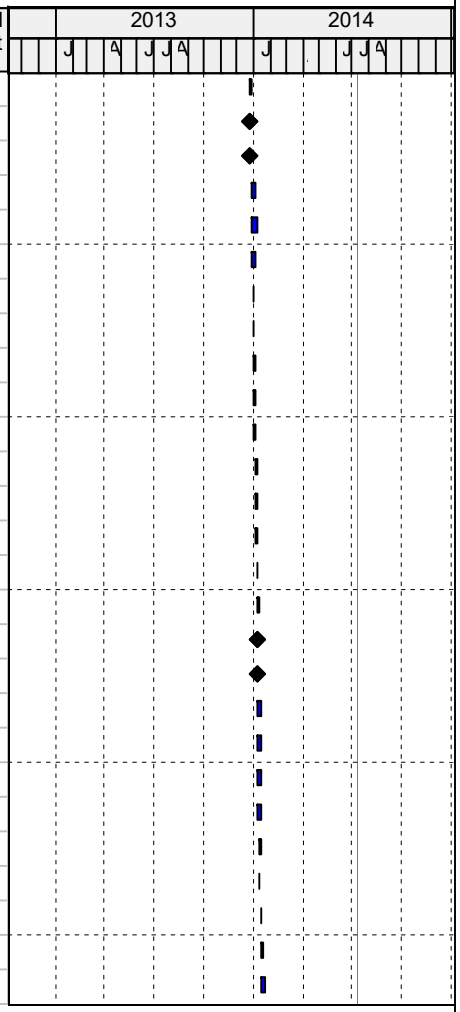



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P18-2006 | MEP Rough In | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2008 | ReSteel / PT Cables | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2010 | Install Edgeform/Embeds | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2012 | Place / Finish Deck | 0 | 0 | 22-Jan-14 A | | |
| P18-2020 | Place Conc @ Core | 0 | 0 | 22-Jan-14 A | | |
| P19-2002 | FRP Columns Below | 5 | 0 | 23-Jan-14 A | 29-Jan-14 A | |
| P19-2000 | Jump/Resteel/Close Core | 4 | 0 | 23-Jan-14 A | 28-Jan-14 A | |
| P19-2004 | Shore / Form Deck | 3 | 0 | 23-Jan-14 A | 27-Jan-14 A | |
| P18-2014 | Stress Tendons | 1 | 0 | 25-Jan-14 A | 25-Jan-14 A | |
| P14–2018 | Remove Reshores | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2006 | MEP Rough In | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2008 | ReSteel / PT Cables | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2010 | Install Edgeform/Embeds | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2012 | Place / Finish Deck | 0 | 0 | 29-Jan-14 A | | |
| P19-2020 | Place Conc @ Core | 0 | 0 | 29-Jan-14 A | | |
| P20-2002 | FRP Columns Below | 5 | 0 | 30-Jan-14 A | 05-Feb-14 A | |
| P20-2000 | Jump/Resteel/Close Core | 9 | 0 | 30-Jan-14 A | 11-Feb-14 A | |
| P20-2004 | Shore / Form Deck | 6 | 0 | 30-Jan-14 A | 10-Feb-14 A | |
| P19-2014 | Stress Tendons | 1 | 0 | 01-Feb-14 A | 01-Feb-14 A | |
| P13A–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P14–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P15–2016 | Strip / ReShore Deck | 3 | 0 | 06-Feb-14 A | 10-Feb-14 A | |
| P20-2006 | MEP Rough In | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2008 | ReSteel / PT Cables | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2010 | Install Edgeform/Embeds | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| L03-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 06-Feb-14 A | 12-Feb-14 A | |
| P16-2016 | Strip / ReShore Deck | 3 | 0 | 10-Feb-14 A | 12-Feb-14 A | |

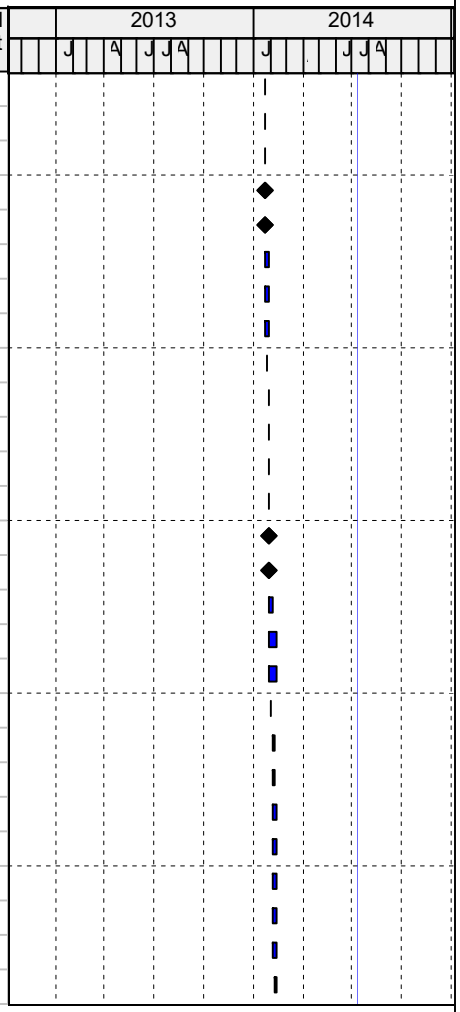



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-2018 | Remove Reshores | 2 | 0 | 10-Feb-14 A | 11-Feb-14 A | |
| L03-2018 | Remove Reshores | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| P17-2016 | Strip / ReShore Deck | 3 | 0 | 12-Feb-14 A | 14-Feb-14 A | |
| P20-2012 | Place / Finish Deck | 0 | 0 | 12-Feb-14 A | | |
| P20-2020 | Place Conc @ Core | 0 | 0 | 12-Feb-14 A | | |
| L04-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-Feb-14 A | 18-Feb-14 A | |
| P12–2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P18-2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P21-2002 | FRP Columns Below | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| P21-2000 | Jump/Resteel/Close Core | 4 | 0 | 13-Feb-14 A | 18-Feb-14 A | |
| P21-2004 | Shore / Form Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P19-2016 | Strip / ReShore Deck | 3 | 0 | 14-Feb-14 A | 18-Feb-14 A | |
| P20-2014 | Stress Tendons | 1 | 0 | 15-Feb-14 A | 15-Feb-14 A | |
| P21-2006 | MEP Rough In | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2008 | ReSteel / PT Cables | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P20-2016 | Strip / ReShore Deck | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| L05-2018 | Remove Reshores | 2 | 0 | 18-Feb-14 A | 19-Feb-14 A | |
| P21-2012 | Place / Finish Deck | 0 | 0 | 19-Feb-14 A | | |
| P21-2020 | Place Conc @ Core | 0 | 0 | 19-Feb-14 A | | |
| P22-2002 | FRP Columns Below | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P22-2000 | Jump/Resteel/Close Core | 4 | 0 | 20-Feb-14 A | 25-Feb-14 A | |
| P22-2004 | Shore / Form Deck | 3 | 0 | 20-Feb-14 A | 24-Feb-14 A | |
| L05-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P21-2014 | Stress Tendons | 1 | 0 | 22-Feb-14 A | 22-Feb-14 A | |
| P21-2016 | Strip / ReShore Deck | 3 | 0 | 24-Feb-14 A | 26-Feb-14 A | |
| P22-2006 | MEP Rough In | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |

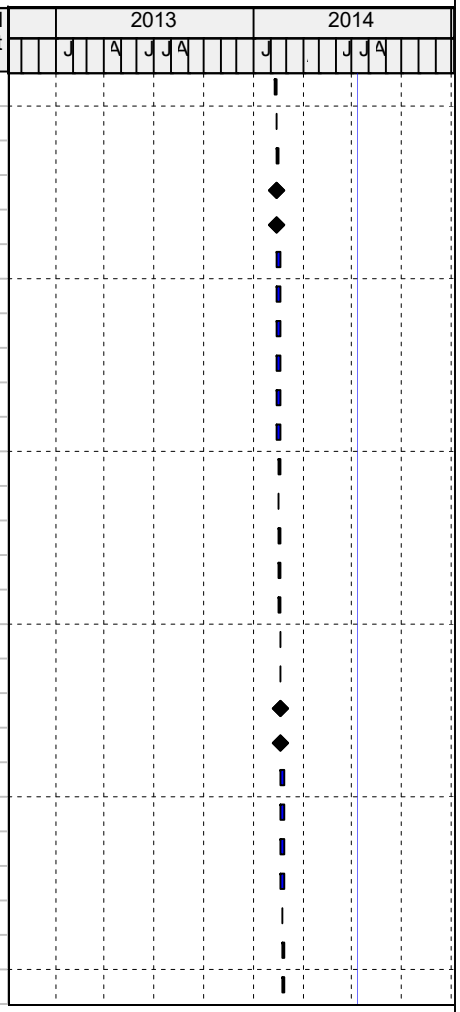



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P22-2008 | ReSteel / PT Cables | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| L06-2018 | Remove Reshores | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| P22-2012 | Place / Finish Deck | 0 | 0 | 26-Feb-14 A | | |
| P22-2020 | Place Conc @ Core | 0 | 0 | 26-Feb-14 A | | |
| P23-2002 | FRP Columns Below | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2000 | Jump/Resteel/Close Core | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2004 | Shore / Form Deck | 3 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2006 | MEP Rough In | 2 | 0 | 01-Mar-14 A | 03-Mar-14 A | |
| P22-2014 | Stress Tendons | 1 | 0 | 01-Mar-14 A | 01-Mar-14 A | |
| P23-2008 | ReSteel / PT Cables | 2 | 0 | 03-Mar-14 A | 04-Mar-14 A | |
| P22-2016 | Strip / ReShore Deck | 3 | 0 | 04-Mar-14 A | 10-Mar-14 A | |
| P23-2010 | Install Edgeform/Embeds | 2 | 0 | 04-Mar-14 A | 04-Mar-14 A | |
| L07-2018 | Remove Reshores | 2 | 0 | 04-Mar-14 A | 05-Mar-14 A | |
| P23-2012 | Place / Finish Deck | 0 | 0 | 05-Mar-14 A | | |
| P23-2020 | Place Conc @ Core | 0 | 0 | 05-Mar-14 A | | |
| P24-2002 | FRP Columns Below | 5 | 0 | 05-Mar-14 A | 07-Mar-14 A | |
| P24-2004 | Shore / Form Deck | 3 | 0 | 06-Mar-14 A | 10-Mar-14 A | |
| P24-2000 | Jump/Resteel/Close Core | 4 | 0 | 08-Mar-14 A | 10-Mar-14 A | |
| P23-2014 | Stress Tendons | 1 | 0 | 10-Mar-14 A | 10-Mar-14 A | |
| P24-2008 | ReSteel / PT Cables | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P24-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P23-2016 | Strip / ReShore Deck | 3 | 0 | 11-Mar-14 A | 17-Mar-14 A | |
| P24-2006 | MEP Rough In | 2 | 0 | 11-Mar-14 A | 11-Mar-14 A | |
| P25-2002 | FRP Columns Below | 5 | 0 | 11-Mar-14 A | 13-Mar-14 A | |
| L08-2018 | Remove Reshores | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| P24-2012 | Place / Finish Deck | 0 | 0 | 12-Mar-14 A | | |

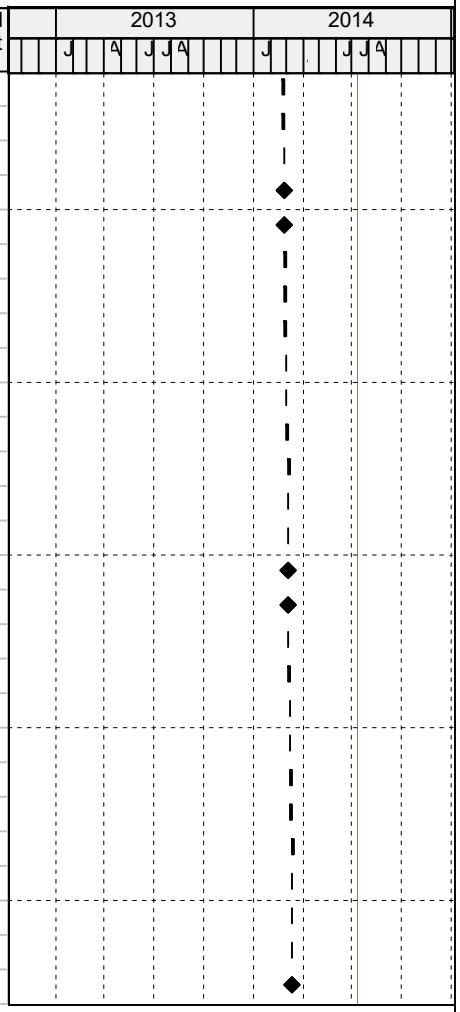



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P24-2020 | Place Conc @ Core | 0 | 0 | 12-Mar-14 A | | |
| P25-2004 | Shore / Form Deck | 3 | 0 | 13-Mar-14 A | 17-Mar-14 A | |
| P25-2000 | Jump/Resteel/Close Core | 4 | 0 | 15-Mar-14 A | 17-Mar-14 A | |
| P24-2014 | Stress Tendons | 1 | 0 | 17-Mar-14 A | 17-Mar-14 A | |
| P25-2006 | MEP Rough In | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2008 | ReSteel / PT Cables | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| L06-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 18-Mar-14 A | 20-Mar-14 A | |
| L09-2018 | Remove Reshores | 2 | 0 | 18-Mar-14 A | 19-Mar-14 A | |
| P26-2002 | FRP Columns Below | 5 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| P25-2012 | Place / Finish Deck | 0 | 0 | 19-Mar-14 A | | |
| P25-2020 | Place Conc @ Core | 0 | 0 | 19-Mar-14 A | | |
| P26-2004 | Shore / Form Deck | 3 | 0 | 20-Mar-14 A | 24-Mar-14 A | |
| L07-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 21-Mar-14 A | 25-Mar-14 A | |
| P26-2000 | Jump/Resteel/Close Core | 4 | 0 | 22-Mar-14 A | 24-Mar-14 A | |
| P26-2006 | MEP Rough In | 2 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P26-2008 | ReSteel / PT Cables | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P26-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P25-2014 | Stress Tendons | 1 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P27-2002 | FRP Columns Below | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| P26-2012 | Place / Finish Deck | 0 | 0 | 26-Mar-14 A | | |
| P26-2020 | Place Conc @ Core | 0 | 0 | 26-Mar-14 A | | |
| L08-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 26-Mar-14 A | 28-Mar-14 A | |
| L10-2018 | Remove Reshores | 2 | 0 | 26-Mar-14 A | 27-Mar-14 A | |
| P27-2004 | Shore / Form Deck | 3 | 0 | 27-Mar-14 A | 31-Mar-14 A | |
| P27-2000 | Jump/Resteel/Close Core | 4 | 0 | 29-Mar-14 A | 31-Mar-14 A | |
| P27-2006 | MEP Rough In | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |

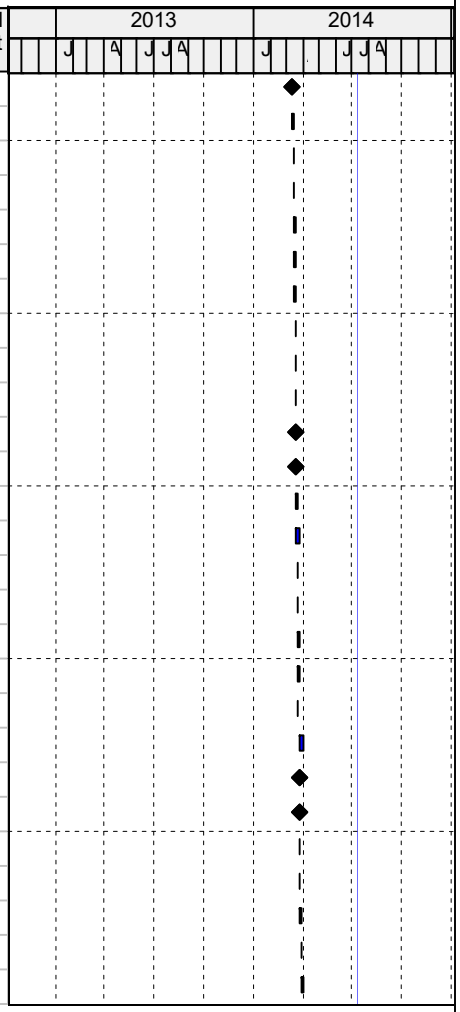



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P27-2008 | ReSteel / PT Cables | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2010 | Install Edgeform/Embeds | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P26-2014 | Stress Tendons | 1 | 0 | 31-Mar-14 A | 31-Mar-14 A | |
| L09-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 31-Mar-14 A | 02-Apr-14 A | |
| P24-2016 | Strip / ReShore Deck | 3 | 0 | 01-Apr-14 A | 07-Apr-14 A | |
| L11-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 02-Apr-14 A | |
| L12-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 03-Apr-14 A | |
| P27-2012 | Place / Finish Deck | 0 | 0 | 02-Apr-14 A | | |
| P27-2020 | Place Conc @ Core | 0 | 0 | 02-Apr-14 A | | |
| P28-2002 | FRP Columns Below | 5 | 0 | 02-Apr-14 A | 04-Apr-14 A | |
| P28-2004 | Shore / Form Deck | 4 | 0 | 03-Apr-14 A | 08-Apr-14 A | |
| L10-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| P27-2014 | Stress Tendons | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| P25-2016 | Strip / ReShore Deck | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L14-2018 | Remove Reshores | 2 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| P28-2000 | Jump/Resteel/Close Core | 7 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| P28-2006 | MEP Rough In | 4 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2008 | ReSteel / PT Cables | 4 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Apr-14 A | 11-Apr-14 A | |
| L12-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| P28-2012 | Place / Finish Deck | 0 | 0 | 14-Apr-14 A | | |
| P28-2020 | Place Conc @ Core | 0 | 0 | 14-Apr-14 A | | |
| P29-2002 | FRP Columns Above Roof Deck | 3 | 0 | 14-Apr-14 A | 18-Apr-14 A | |
| P26-2016 | Strip / ReShore Deck | 3 | 0 | 14-Apr-14 A | 17-Apr-14 A | |
| L14-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-Apr-14 A | 18-Apr-14 A | |
| P28-2014 | Stress Tendons | 1 | 0 | 17-Apr-14 A | 17-Apr-14 A | |

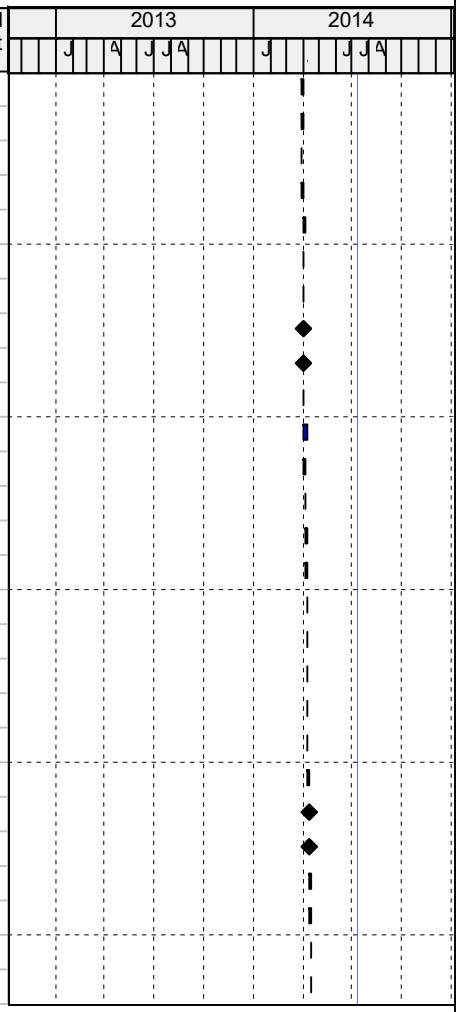



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P29-2000 | Strip Core | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| P27-2016 | Strip / ReShore Deck | 3 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L15-2018 | Remove Reshores | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| P28-2016 | Strip / ReShore Deck | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L15-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L16-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-May-14 A | 19-May-14 A | |
| L16-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2019 | Grind Ceiling for Skim Coat | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| **Ballroom Catwalk & Roof** | | | | | | |
| PC-2100 | Erect Structural Steel @ Porte Cochere | 3 | 0 | 30-Jan-14 A | 03-Feb-14 A | |
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 7 | 0 | 07-Feb-14 A | 17-Feb-14 A | |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| PC-2102 | Metal Decking @ Porte Cochere/ Roof | 2 | 0 | 17-Apr-14 A | 18-Apr-14 A | |
| BR-2112 | BR - Fireproofing @ Structural Steel | 2 | 0 | 27-May-14 A | 30-May-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Mech Penthouse** | | | | | | |
| PH-8706 | Set Mech Equipment @ Tower Roof | 3 | 0 | 22-May-14 A | 28-May-14 A | |
| PH-8708 | Set Equipment @ Penthouse | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| PH-8700 | PH - Structural Steel and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| **Vertical Circulation** | | | | | | |
| **Stairs** | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 25-Nov-13 A | 26-Nov-13 A | |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 27-Nov-13 A | 03-Dec-13 A | |
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 04-Dec-13 A | 05-Dec-13 A | |
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 06-Dec-13 A | 09-Dec-13 A | |

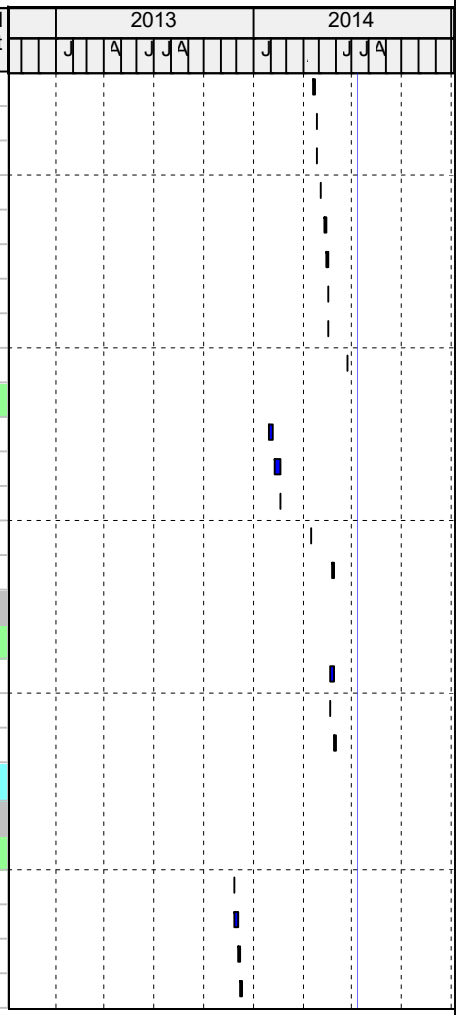



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 2 | 0 | 03-Feb-14 A | 04-Feb-14 A | |
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 2 | 0 | 06-Feb-14 A | 07-Feb-14 A | |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 2 | 0 | 07-Feb-14 A | 07-Feb-14 A | |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 2 | 0 | 07-Feb-14 A | 10-Feb-14 A | |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 2 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 2 | 0 | 06-Mar-14 A | 07-Mar-14 A | |
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 2 | 0 | 07-Mar-14 A | 10-Mar-14 A | |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 2 | 0 | 13-Mar-14 A | 14-Mar-14 A | |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 2 | 0 | 08-Apr-14 A | 21-Apr-14 A | |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| S1-4040 | Stair 1 - Set Mtl Stairs / Railings L18 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 10-Dec-13 A | 11-Dec-13 A | |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 12-Dec-13 A | 13-Dec-13 A | |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 16-Dec-13 A | 17-Dec-13 A | |
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 18-Dec-13 A | 19-Dec-13 A | |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 2 | 0 | 12-Feb-14 A | 13-Feb-14 A | |
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 2 | 0 | 13-Feb-14 A | 13-Feb-14 A | |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 2 | 0 | 13-Feb-14 A | 14-Feb-14 A | |
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 2 | 0 | 19-Feb-14 A | 20-Feb-14 A | |

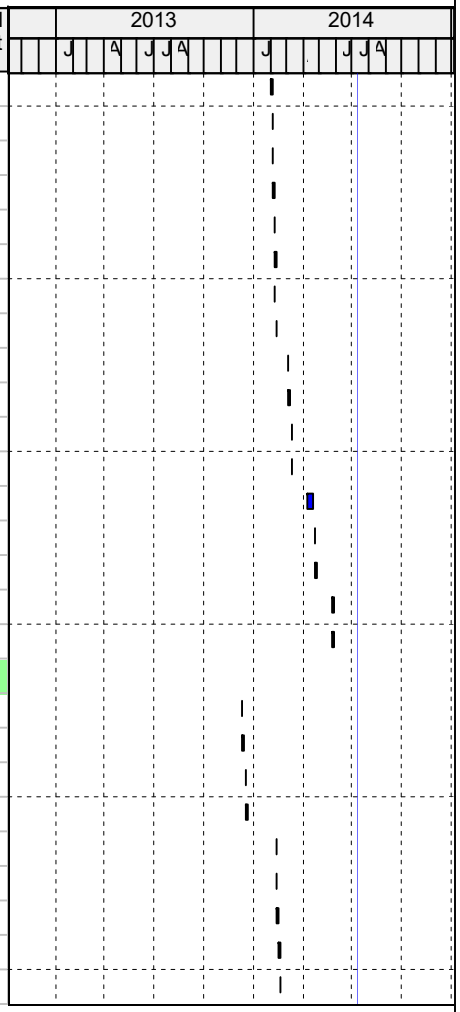



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 2 | 0 | 21-Feb-14 A | 24-Feb-14 A | |
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 2 | 0 | 19-Mar-14 A | 20-Mar-14 A | |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 2 | 0 | 21-Mar-14 A | 22-Mar-14 A | |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 2 | 0 | 14-May-14 A | 15-May-14 A | |
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 2 | 0 | 16-May-14 A | 19-May-14 A | |
| S2-4038 | Stair 2 - Set Mtl Stairs / Railings L17 | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - Set Metal Stairs / Railings LL2 | 6 | 0 | 05-Mar-14 A | 20-Mar-14 A | |
| S3-4002 | Stair 3 - Set Metal Stairs / Railings LL1 | 6 | 0 | 17-Mar-14 A | 21-Mar-14 A | |
| S3-4004 | Stair 3 - Permanent Railings / Final Finishes | 4 | 4 | 14-Jul-14 | 17-Jul-14 | 102 |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |
| S4-4000 | Stair 4 - Set Metal Stairs / Railings LL2 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4002 | Stair 4 - Set Metal Stairs / Railings LL1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4004 | Stair 4 -Set Metal Stairs / Railings L1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4006 | Stair 4 - Permanent Railings / Final Finishes | 4 | 4 | 14-Jul-14 | 17-Jul-14 | 102 |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |
| S6-4000 | Stair 6 - Set Metal Stairs / Railings | 5 | 0 | 25-Jun-14 A | 01-Jul-14 A | |
| S6-4002 | Stair 6 - Permanent Railings / Final Finishes | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 103 |
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 4 | 14-Jul-14 | 17-Jul-14 | 107 |
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 0 | 14-Apr-14 A | 25-Apr-14 A | |

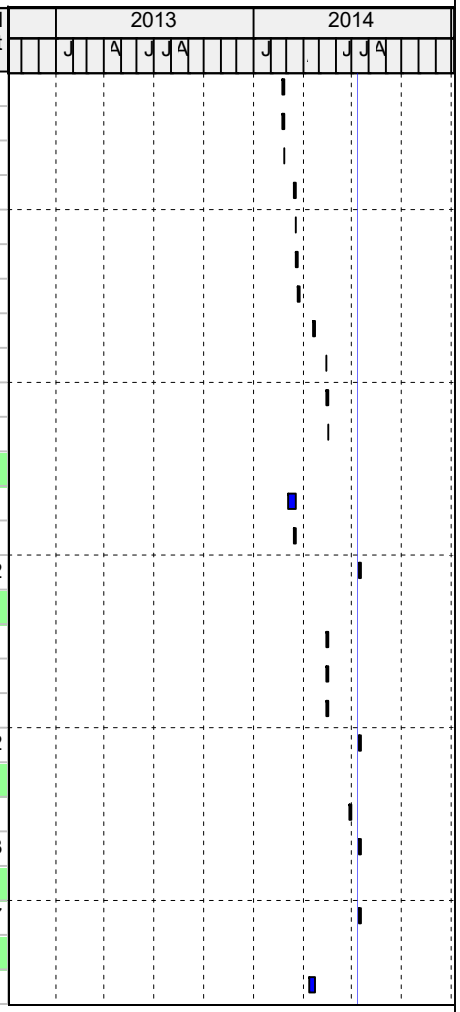



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes | 5 | 5 | 15-Jul-14 | 21-Jul-14 | 100 |
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a -Set Metal Stairs / Railings L1 | 5 | 5 | 14-Jul-14 | 18-Jul-14 | 99 |
| S4a-4002 | Stair 4a - Permanent Railings / Final Finishes | 2 | 2 | 21-Jul-14 | 22-Jul-14 | 99 |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 07-Jun-13 A | | |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 0 | 17-Jun-13 A | 21-Jun-13 A | |
| EL-1004 | Elev - Submittal Approval | 21 | 0 | 21-Jun-13 A | 01-Jan-14 A | |
| EL-1006 | Elev - Release to Manufacturing | 14 | 0 | 02-Jan-14 A | 15-Jan-14 A | |
| EL-1008 | Elev - Fabrication (Engineered Geared) | 95 | 0 | 16-Jan-14 A | 14-Jun-14 A | |
| EL-1010 | Elev - Machines delivered | 1 | 0 | 12-May-14 A | 12-May-14 A | |
| EL-1011 | Elev - Elevator Machines Flown & Set At Top Of Hoist | 5 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5016 | Elev 5 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-1216 | Elev 1&2 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-3416 | Elev 3&4 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-1202 | Elev 1&2 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-3402 | Elev 3&4 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-5018 | Elev 5 - Set Hoistway Machines | 3 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| EL-1218 | Elev 1&2 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-3418 | Elev 3&4 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-1200 | Elev 1&2 - Hoistway Clear & Ready (GC) | 0 | 0 | 20-Jun-14 A | | |
| EL-1204 | Elev 1&2 - Install Rails & Brackets | 17 | 0 | 23-Jun-14 A | 07-Jul-14 A | |
| EL-3400 | Elev 3&4 - Hoistway Clear & Ready (GC) | 0 | 0 | 23-Jun-14 A | | |
| EL-3404 | Elev 3&4 - Install Rails & Brackets | 18 | 2 | 24-Jun-14 A | 15-Jul-14 | 20 |
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 24-Jun-14 A | | |

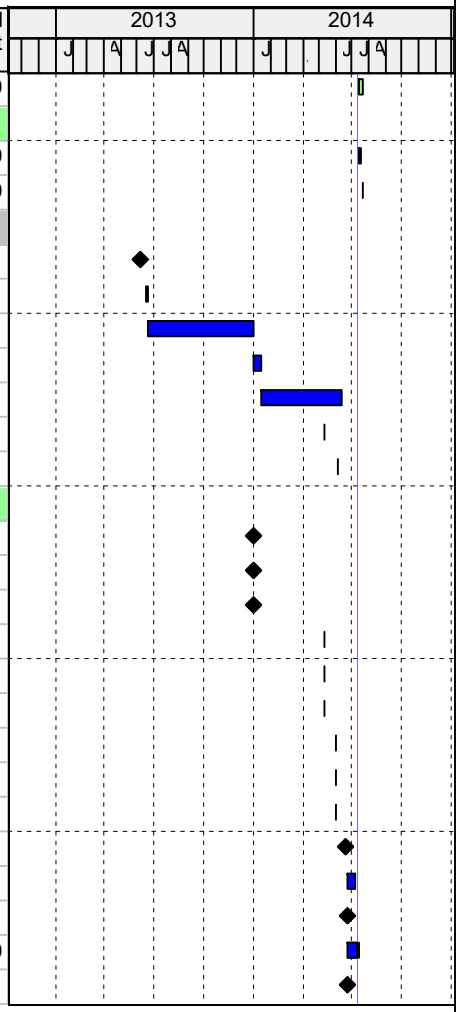


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-1206 | Elev 1&2 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 14-Jul-14 | 24 |
| EL-1207 | Elev 1&2 - Install Pit Equipment/Car Sling/CWT Fram | 3 | 3 | 14-Jul-14 | 17-Jul-14 | 24 |
| EL-3406 | Elev 3&4 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Jul-14 | 20 |
| EL-3407 | Elev 3&4 - Install Pit Equipment/Car Sling/CWT Fram | 5 | 5 | 16-Jul-14 | 22-Jul-14 | 20 |
| EL-1208 | Elev 1&2 - Install MHoist & Cable | 5 | 5 | 17-Jul-14 | 24-Jul-14 | 24 |
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 18-Jul-14 | | 22 |
| EL-5004 | Elev 5 - Install Rails & Brackets | 13 | 13 | 18-Jul-14 | 05-Aug-14 | 17 |
| EL-3408 | Elev 3&4 - Install Hoist & Cable | 5 | 5 | 23-Jul-14 | 29-Jul-14 | 20 |
| EL-1210 | Elev 1&2 - Install Entrances/Doors/Fixtures/Fascia | 19 | 19 | 24-Jul-14 | 20-Aug-14 | 24 |
| EL-3410 | Elev 3&4 - Install Entrances/Doors/Fixtures/Fascia | 30 | 30 | 30-Jul-14 | 10-Sep-14 | 20 |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 2 | 2 | 01-Aug-14* | 04-Aug-14 | 60 |
| EL-6018 | Elev 6 - Set Hoistway Machines | 2 | 2 | 05-Aug-14 | 06-Aug-14 | 60 |
| EL-5006 | Elev 5 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 05-Aug-14 | 17 |
| EL-5007 | Elev 5 - Install Pit Equipment/Car Sling/CWT Frame/V | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 17 |
| EL-6016 | Elev 6 - Hoistway Walls Complete (GC) | 0 | 0 | | 06-Aug-14 | 60 |
| EL-6004 | Elev 6 - Install Cylinders/Rails & Brackets | 4 | 4 | 07-Aug-14 | 12-Aug-14 | 60 |
| EL-6006 | Elev 6 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 12-Aug-14 | 60 |
| EL-5008 | Elev 5 - Install MHoist & Cable | 4 | 4 | 13-Aug-14 | 18-Aug-14 | 17 |
| EL-6007 | Elev 6 - Install Pit Equipment/Car Sling | 3 | 3 | 13-Aug-14 | 15-Aug-14 | 60 |
| EL-6010 | Elev 6 - Install Entrances/Doors/Fixtures/Fascia | 3 | 3 | 18-Aug-14 | 20-Aug-14 | 60 |
| EL-5010 | Elev 5 - Install Entrances/Doors/Fixtures/Fascia | 21 | 21 | 19-Aug-14 | 17-Sep-14 | 17 |
| EL-1212 | Elev 1&2 - Install Hoistway Equipment/Pipe & Wire | 17 | 17 | 20-Aug-14 | 15-Sep-14 | 36 |
| EL-6012 | Elev 6 - Install Hoistway Equipment/Pipe & Wire | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 60 |
| EL-6014 | Elev 6 - Install Cab/Wiring/Door Operator(s) | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 60 |
| EL-6022 | Elev 6 - Adjust | 5 | 5 | 02-Sep-14 | 08-Sep-14 | 60 |
| EL-6024 | Elev 6 - Clean / Paint / Punchlist | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 60 |
| EL-6026 | Elev 6 - Inspections | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 88 |

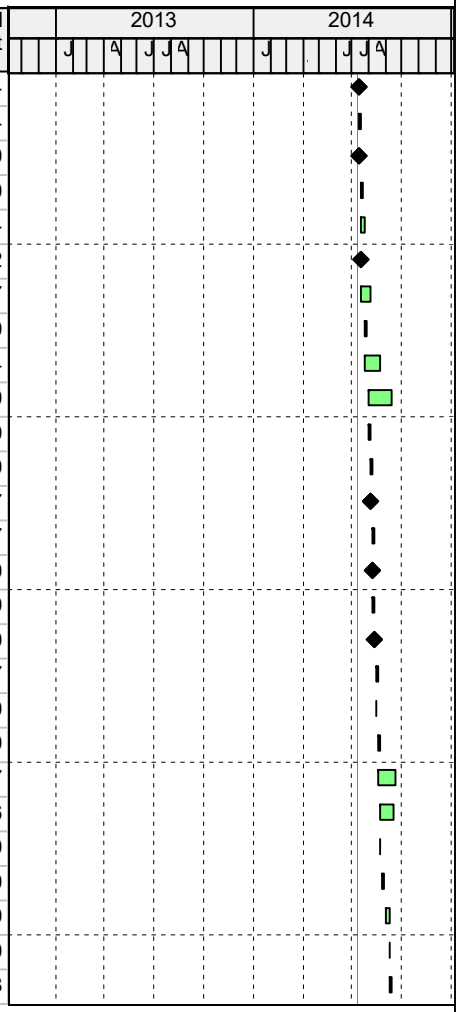



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-3412 | Elev 3&4 - Install Hoistway Equipment/Pipe & Wire | 23 | 23 | 11-Sep-14 | 13-Oct-14 | 23 |
| EL-1214 | Elev 1&2 - Install Cab/Wiring/Door Operator(s) | 16 | 16 | 15-Sep-14 | 07-Oct-14 | 36 |
| EL-5012 | Elev 5 - Install Hoistway Equipment/Pipe & Wire | 14 | 14 | 18-Sep-14 | 07-Oct-14 | 17 |
| EL-1222 | Elev 1&2 - Adjust | 5 | 5 | 07-Oct-14 | 14-Oct-14 | 36 |
| EL-5014 | Elev 5 - Install Cab/Wiring/Door Operator(s) | 7 | 7 | 08-Oct-14 | 16-Oct-14 | 17 |
| EL-3414 | Elev 3&4 - Install Cab/Wiring/Door Operator(s) | 10 | 10 | 14-Oct-14 | 27-Oct-14 | 23 |
| EL-1224 | Elev 1&2 - Clean / Paint / Punchlist | 3 | 3 | 14-Oct-14 | 17-Oct-14 | 36 |
| EL-5022 | Elev 5 - Adjust | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 17 |
| EL-1226 | Elev 1&2 - Inspections | 2 | 2 | 17-Oct-14 | 19-Oct-14 | 55 |
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 3 | 3 | 24-Oct-14 | 28-Oct-14 | 17 |
| EL-3422 | Elev 3&4 - Adjust | 5 | 5 | 28-Oct-14 | 03-Nov-14 | 23 |
| EL-5026 | Elev 5 - Inspections | 2 | 2 | 29-Oct-14 | 30-Oct-14 | 26 |
| EL-3424 | Elev 3&4 - Clean / Paint / Punchlist | 3 | 3 | 04-Nov-14 | 06-Nov-14 | 23 |
| EL-3426 | Elev 3&4 - Inspections | 2 | 2 | 07-Nov-14 | 08-Nov-14 | 36 |
| **Exterior Shell** | | | | | | |
| **Elevations** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2** | | | | | | |
| L3D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Feb-14 A | 12-Feb-14 A | |
| L3-5308 | L3- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 17-Feb-14 A | 21-Feb-14 A | |
| L4D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Feb-14 A | 19-Feb-14 A | |
| L4-5308 | L4- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Feb-14 A | 28-Feb-14 A | |
| L5D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Feb-14 A | 26-Feb-14 A | |
| L5-5308 | L5- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 03-Mar-14 A | 07-Mar-14 A | |
| L6D5308 | Deliver/Stock Wall Panels | 1 | 0 | 05-Mar-14 A | 05-Mar-14 A | |
| L6-5308 | L6- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L7-5308 | L7- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 12-Mar-14 A | 21-Mar-14 A | |

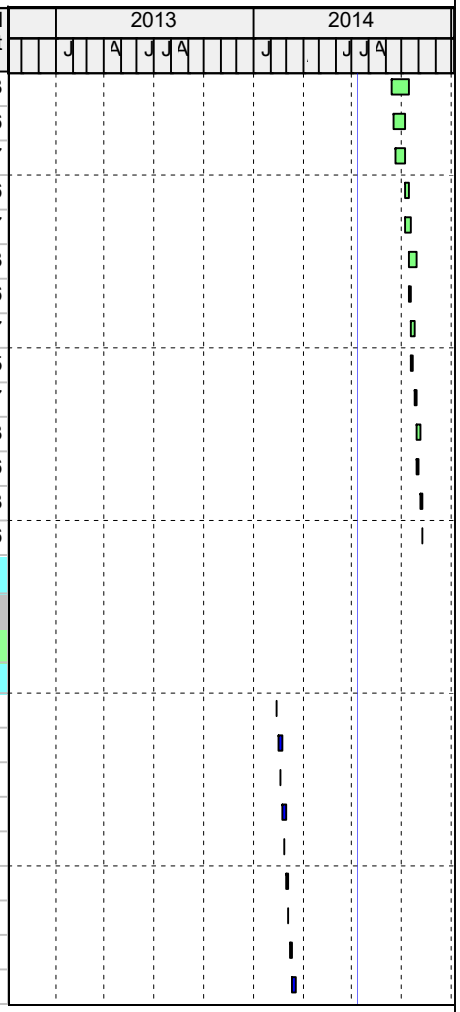



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L7D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Mar-14 A | 12-Mar-14 A | |
| L8D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Mar-14 A | 19-Mar-14 A | |
| L8-5308 | L8- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Mar-14 A | 28-Mar-14 A | |
| L9D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L9-5308 | L9- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 31-Mar-14 A | 07-Apr-14 A | |
| 10D5308 | Deliver/Stock Wall Panels | 1 | 0 | 02-Apr-14 A | 02-Apr-14 A | |
| L10-5308 | L10- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 07-Apr-14 A | 11-Apr-14 A | |
| 11D5308 | Deliver/Stock Wall Panels | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L11-5308 | L11- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 11-Apr-14 A | 18-Apr-14 A | |
| 12D5308 | Deliver/Stock Wall Panels | 1 | 0 | 16-Apr-14 A | 16-Apr-14 A | |
| L12-5308 | L12- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Apr-14 A | 25-Apr-14 A | |
| 14D5308 | Deliver/Stock Wall Panels | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L14-5308 | L14 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Apr-14 A | 01-May-14 A | |
| 15D5308 | Deliver/Stock Wall Panels | 1 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L15-5308 | L15 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| 16D5308 | Deliver/Stock Wall Panels | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L16-5308 | L16- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| 17D5308 | Deliver/Stock Wall Panels | 1 | 0 | 14-May-14 A | 14-May-14 A | |
| L17-5308 | L17 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 20-May-14 A | 11-Jun-14 A | |
| LL2-5308 | LL2 Thru L4 - Support Frame/Sheathing for Metal Wa | 6 | 6 | 19-Jun-14 A | 21-Jul-14 | 21 |
| LL1-5308 | LL1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 6 | 19-Jun-14 A | 21-Jul-14 | 21 |
| L1-5308 | L1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 6 | 19-Jun-14 A | 21-Jul-14 | 21 |
| **Level 1** | | | | | | |
| L1-5102 | L1 - Storefront Frames | 9 | 9 | 22-Jul-14 | 01-Aug-14 | 21 |
| L1-5104 | L1 - Storefront Glazing | 4 | 4 | 04-Aug-14 | 07-Aug-14 | 21 |
| EP-5110 | L1 - Revolving Doors | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 44 |
| L3-5102 | L3- Storefront Frames | 7 | 7 | 15-Aug-14 | 25-Aug-14 | 30 |

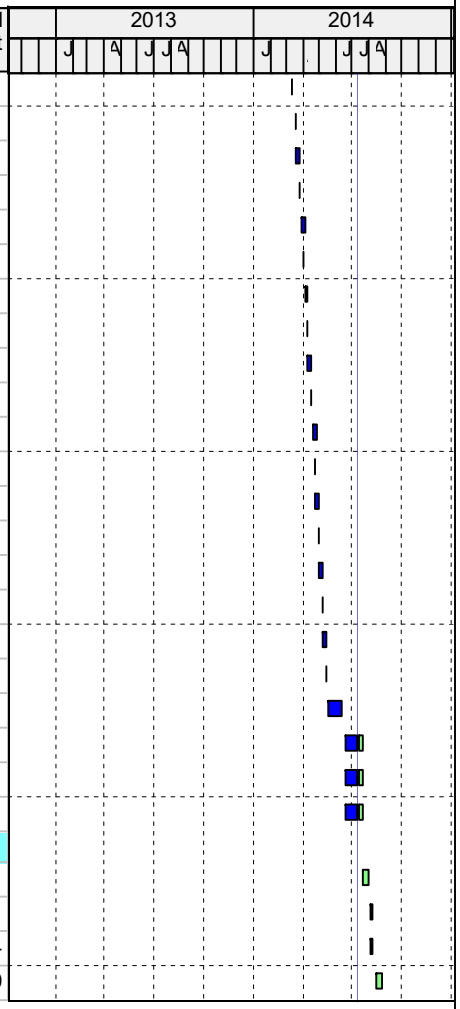



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L3-5104 | L3 - Storefront Glazing | 3 | 3 | 26-Aug-14 | 28-Aug-14 | 30 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Levels 3-4** | | | | | | |
| L3-5130 | L3 - Install Punch Windows | 5 | 0 | 24-Feb-14 A | 10-Mar-14 A | |
| L4-5130 | L4 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 12-Mar-14 A | |
| L5-5130 | L5 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L6-5130 | L6- Install Punch Windows | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L7-5130 | L7 - Install Punch Windows | 5 | 0 | 18-Mar-14 A | 21-Mar-14 A | |
| L8-5130 | L8 - Install Punch Windows | 5 | 0 | 24-Mar-14 A | 28-Mar-14 A | |
| L9-5130 | L9 - Install Punch Windows | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L10-5130 | L10 - Install Punch Windows | 5 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-5130 | L11 - Install Punch Windows | 5 | 0 | 14-Apr-14 A | 21-Apr-14 A | |
| L12-5130 | L12 - Install Punch Windows | 5 | 0 | 22-Apr-14 A | 25-Apr-14 A | |
| L14-5130 | L14 - Install Punch Windows | 5 | 0 | 28-Apr-14 A | 05-May-14 A | |
| L15-5130 | L15 - Install Punch Windows | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| L16-5130 | L16 - Install Punch Windows | 5 | 0 | 12-May-14 A | 20-May-14 A | |
| L17-5130 | L17 - Install Punch Windows | 5 | 0 | 27-May-14 A | 16-Jun-14 A | |
| Roofs | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 34 |
| RF-4026 | L1 - City Park - Protection Board | 3 | 3 | 18-Aug-14 | 20-Aug-14 | 34 |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 34 |
| **Pool Membrane - (elev 18')** | | | | | | |
| RF-4034 | Pool Waterproofing / Membrane | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 41 |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |
| RF-4010 | AR - Set Mechanical Equipment | 5 | 0 | 10-Jun-14 A | 12-Jun-14 A | |
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 12 | 12 | 17-Jul-14 | 01-Aug-14 | 34 |

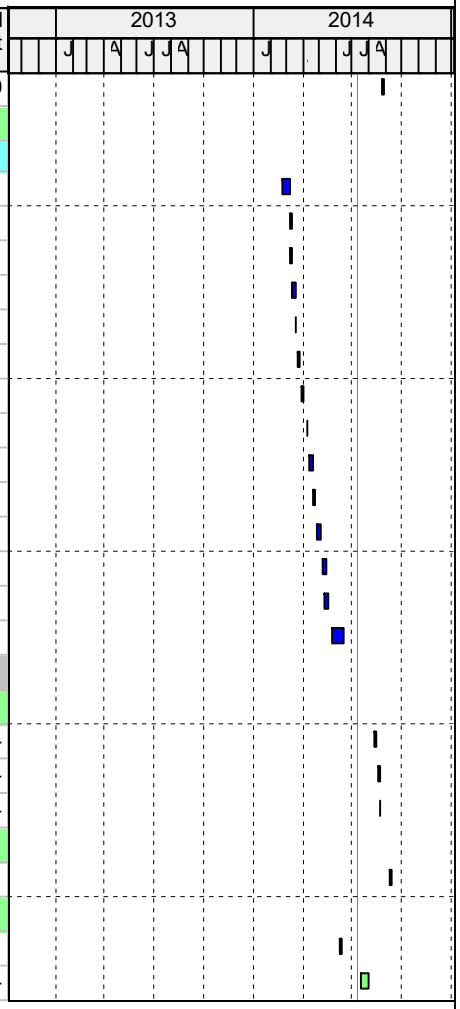



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| RF-4012 | AR - Coping / Flashing | 4 | 4 | 04-Aug-14 | 07-Aug-14 | 92 |
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 34 |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |
| PC-4008 | RF - Entry / Porte Cochere Roofing System | 6 | 6 | 25-Jul-14 | 01-Aug-14 | 34 |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | RF - Upper Ballroom Roofing System | 3 | 3 | 22-Jul-14 | 24-Jul-14 | 34 |
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 4 | 4 | 25-Jul-14 | 30-Jul-14 | 34 |
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |
| RF-4018 | TR - Terrace Roof - Roofing System | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 79 |
| RF-4020 | TR - Terrace Roof - Coping / Flashing | 3 | 3 | 11-Aug-14 | 13-Aug-14 | 86 |
| RF-4022 | TR - Terrace Roof - Glass Railing | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 79 |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Perimeter Framing / Sul | 10 | 0 | 02-Jun-14 A | 08-Jul-14 A | |
| RF-4002 | Tower Roof - Roofing System | 8 | 8 | 15-Jul-14 | 24-Jul-14 | 16 |
| **PH - Roof - (elev 173')** | | | | | | |
| RF-4030 | PH - Roofing System | 8 | 8 | 15-Jul-14 | 24-Jul-14 | 16 |
| RF-4032 | PH - Coping / Flashing | 3 | 3 | 25-Jul-14 | 29-Jul-14 | 88 |
| **Rough-In's** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6002 | LL4 - Layout | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| LL4-6008 | LL4 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL4-6012 | LL4 - Fire Sprinkler RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6014 | LL4 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6018 | LL4 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |

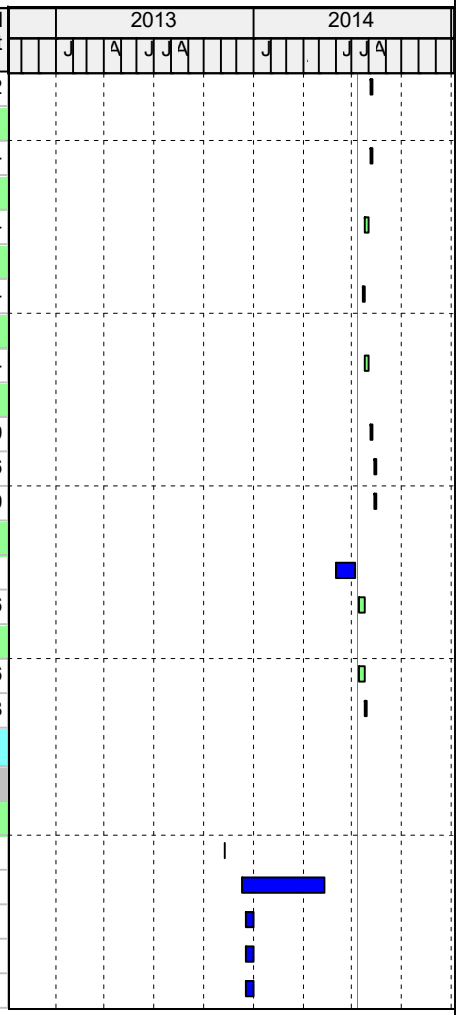



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-6004 | LL4 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL4-6016 | LL4 - Electrical RI | 10 | 2 | 01-May-14 A | 15-Jul-14 | 37 |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties RI | 8 | 2 | 01-May-14 A | 15-Jul-14 | 37 |
| LL4-6010 | LL4 - Elevator pits | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| LL4-6020 | LL4 - H Mtl Frames | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 37 |
| LL4-6024 | LL4 - Inspections | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 37 |
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6002 | LL3 - Layout | 1 | 0 | 19-Nov-13 A | 19-Nov-13 A | |
| LL3-6008 | LL3 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL3-6012 | LL3 - Fire Sprinkler RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6014 | LL3 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6018 | LL3 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6004 | LL3 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL3-6020 | LL3 - H Mtl Frames | 3 | 0 | 08-May-14 A | 09-May-14 A | |
| LL3-6010 | LL3 - F/P Curbs | 5 | 0 | 19-May-14 A | 19-May-14 A | |
| LL3-6016 | LL3 - Electrical RI | 2 | 2 | 26-Jun-14 A | 17-Jul-14 | 38 |
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties RI | 8 | 2 | 26-Jun-14 A | 17-Jul-14 | 38 |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 40 |
| LL3-6024 | LL3 - Inspections | 2 | 2 | 18-Jul-14 | 21-Jul-14 | 38 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6002 | LL2 - Layout | 1 | 0 | 14-Jan-14 A | 14-Jan-14 A | |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| LL2-6012 | LL2 - Fire Sprinkler RI | 10 | 0 | 21-Jan-14 A | 03-Feb-14 A | |
| LL2-6014 | LL2 - Plumbing RI | 10 | 0 | 21-Jan-14 A | 14-Feb-14 A | |
| LL2E-6016 | LL2 - Electrical RI | 8 | 0 | 03-Feb-14 A | 17-Mar-14 A | |
| LL2-6016 | LL2 - Electrical RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |

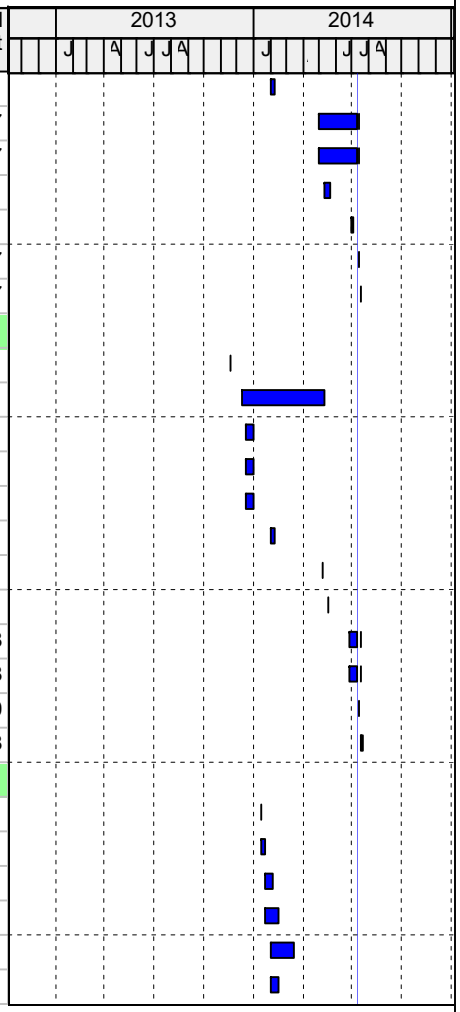



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-6018 | LL2 - HVAC RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2–6004 | LL2 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL2E-6004 | LL2 - CMU Walls | 10 | 0 | 04-Mar-14 A | 09-May-14 A | |
| LL2E-6012 | LL2 - Fire Sprinkler RI | 8 | 0 | 21-Mar-14 A | 01-Apr-14 A | |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 24-Apr-14 A | |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 3 | 6 | 23-Apr-14 A | 21-Jul-14 | 21 |
| LL2E-6020 | LL2 - H Mtl Frames | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| LL2-6020 | LL2 - H Mtl Frames | 3 | 0 | 12-May-14 A | 13-May-14 A | |
| LL2E-6008 | LL2 - Int Wall Framing | 5 | 0 | 13-May-14 A | 22-Jun-14 A | |
| LL2E-6014 | LL2 - Plumbing RI | 8 | 0 | 13-May-14 A | 30-May-14 A | |
| LL2E-6018 | LL2 - HVAC RI | 8 | 2 | 13-May-14 A | 23-Jul-14 | 49 |
| LL2E-6022 | LL2 - Fire Alarm / Elec Specialties RI | 8 | 3 | 13-May-14 A | 24-Jul-14 | 48 |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties RI | 8 | 2 | 19-May-14 A | 15-Jul-14 | 42 |
| LL2-6015 | LL2 - Main Elect Room Set Equip / RI - Power to Ma | 15 | 11 | 30-Jun-14 A | 05-Aug-14 | 79 |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 4 | 16-Jul-14 | 21-Jul-14 | 38 |
| LL2-6024 | LL2 - Inspections | 2 | 2 | 22-Jul-14 | 23-Jul-14 | 38 |
| LL2-6010 | LL2 - F/P Curbs @ Parking | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 58 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6002 | Layout | 3 | 0 | 03-Jan-14 A | 08-Jan-14 A | |
| LL1-6008 | Int Wall Framing & Inspection | 6 | 1 | 08-Jan-14 A | 14-Jul-14 | 15 |
| LL1-Z2-6002 | Layout | 3 | 0 | 08-Jan-14 A | 14-Jan-14 A | |
| LL1-Z3-6002 | Layout | 3 | 0 | 14-Jan-14 A | 17-Jan-14 A | |
| LL1-Z2-6008 | Int Wall Framing & Inspection | 6 | 0 | 17-Jan-14 A | 07-Apr-14 A | |
| LL1-Z3-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-Jan-14 A | 04-Feb-14 A | |
| LL1-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 09-May-14 A | |
| LL1-Z2-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 28-Apr-14 A | |

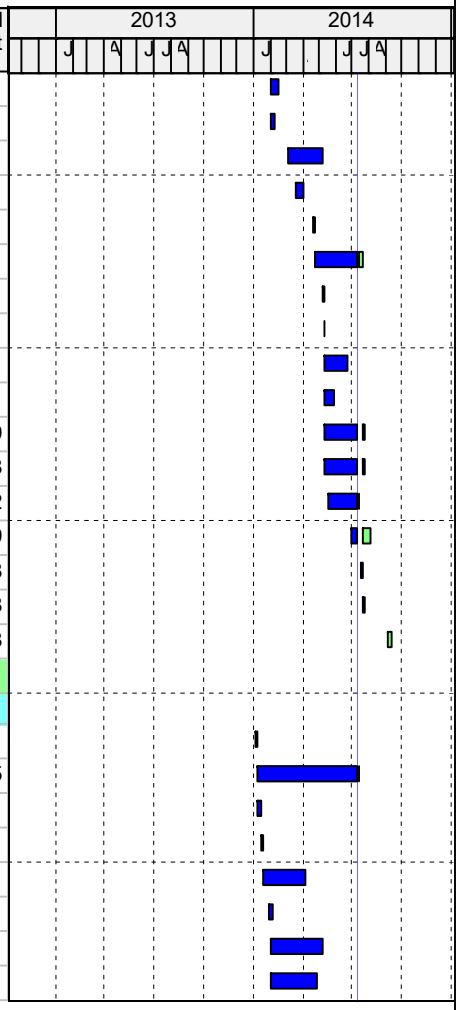



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-6004 | CMU Walls (At All Areas North of Q-Line) | 3 | 0 | 03-Feb-14 A | 13-May-14 A | |
| LL1C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 1 | 17-Feb-14 A | 29-Jul-14 | 21 |
| LL1C-6016 | Complete Electrical RI @ Ceilings | 5 | 1 | 17-Feb-14 A | 30-Jul-14 | 21 |
| LL1C-6018 | Complete HVAC RI @ Ceilings | 5 | 1 | 17-Feb-14 A | 29-Jul-14 | 22 |
| LL1C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 1 | 17-Feb-14 A | 30-Jul-14 | 21 |
| LL1-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 30-Apr-14 A | |
| LL1-6016 | Electrical RI | 20 | 6 | 17-Feb-14 A | 21-Jul-14 | 15 |
| LL1-6018 | HVAC RI | 20 | 8 | 17-Feb-14 A | 23-Jul-14 | 15 |
| LL1-6022 | Fire Alarm / Elec Specialties RI | 20 | 6 | 17-Feb-14 A | 21-Jul-14 | 15 |
| LL1-Z2-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z2-6014 | Plumbing RI | 20 | 4 | 17-Feb-14 A | 17-Jul-14 | 15 |
| LL1-Z2-6016 | Electrical RI | 20 | 4 | 17-Feb-14 A | 17-Jul-14 | 15 |
| LL1-Z2-6018 | HVAC RI | 20 | 4 | 17-Feb-14 A | 17-Jul-14 | 15 |
| LL1-Z2-6022 | Fire Alarm / Elec Specialties RI | 20 | 4 | 17-Feb-14 A | 17-Jul-14 | 15 |
| LL1-Z3-6012 | Fire Sprinkler RI (At All Areas North of Q-Line) | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z3-6014 | Plumbing RI (At All Areas North of Q-Line) | 20 | 8 | 17-Feb-14 A | 24-Jul-14 | 17 |
| LL1-Z3-6016 | Electrical RI (At All Areas North of Q-Line) | 20 | 6 | 17-Feb-14 A | 22-Jul-14 | 19 |
| LL1-Z3-6018 | HVAC RI (At All Areas North of Q-Line) | 20 | 4 | 17-Feb-14 A | 18-Jul-14 | 21 |
| LL1-Z3-6022 | Fire Alarm / Elec Specialties RI (At All Areas North of | 20 | 4 | 17-Feb-14 A | 18-Jul-14 | 21 |
| LL1-Z2C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 1 | 24-Feb-14 A | 01-Aug-14 | 16 |
| LL1-Z2C-6014 | Complete Plumbing RI @ Ceilings | 5 | 1 | 24-Feb-14 A | 01-Aug-14 | 15 |
| LL1-Z2C-6016 | Complete Electrical RI @ Ceilings | 5 | 1 | 24-Feb-14 A | 04-Aug-14 | 15 |
| LL1-Z2C-6018 | Complete HVAC RI @ Ceilings | 5 | 1 | 24-Feb-14 A | 04-Aug-14 | 15 |
| LL1-Z2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 1 | 24-Feb-14 A | 04-Aug-14 | 15 |
| LL1-Z2-6020 | Hollow Metal Door Frames | 5 | 0 | 17-Mar-14 A | 04-Apr-14 A | |
| LL1-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Mar-14 A | 04-Apr-14 A | |

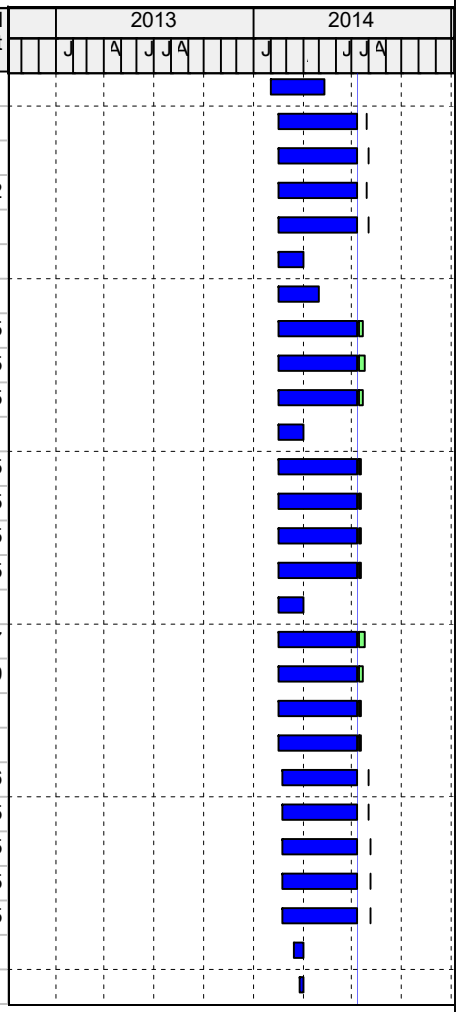



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-6020 | Hollow Metal Door Frames (At All Areas North of Q-Lir | 1 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| L1B-6004 | CMU Walls [including East Service Corridor] | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L1L-6002 | Layout [including back of house] | 3 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 29-Apr-14 A | |
| L1B-6008 | Int Wall Framing & Inspection [including East Service | 6 | 2 | 21-Apr-14 A | 15-Jul-14 | 21 |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 5 | 6 | 25-Apr-14 A | 21-Jul-14 | 21 |
| LL1C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L1K-6004 | CMU Walls [including public restroom] | 3 | 0 | 05-May-14 A | 08-May-14 A | |
| L1K-6002 | Layout [including public restroom] | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| L1K-6008 | Int Wall Framing & Inspection [including public restroc | 4 | 2 | 09-May-14 A | 15-Jul-14 | 8 |
| LL1-6009 | Frame Ceilings | 10 | 4 | 12-May-14 A | 28-Jul-14 | 21 |
| L1B-6002 | Layout [including East Service Corridor] | 3 | 0 | 14-May-14 A | 27-May-14 A | |
| L1L-6008 | Int Wall Framing & Inspection [including back of hous | 6 | 4 | 27-May-14 A | 17-Jul-14 | 4 |
| L1L-6004 | CMU Walls [including back of house] | 3 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L1K-6012 | Fire Sprinkler RI [including public restroom] | 10 | 6 | 02-Jun-14 A | 24-Jul-14 | 11 |
| L1K-6014 | Plumbing RI [including public restroom] | 10 | 6 | 02-Jun-14 A | 24-Jul-14 | 8 |
| L1K-6016 | Electrical RI [including public restroom] | 10 | 6 | 02-Jun-14 A | 24-Jul-14 | 8 |
| L1K-6018 | HVAC RI [including public restroom] | 10 | 6 | 02-Jun-14 A | 24-Jul-14 | 11 |
| L1B-6014 | Plumbing RI [including East Service Corridor] | 10 | 0 | 16-Jun-14 A | 24-Jun-14 A | |
| L1B-6018 | HVAC RI [including East Service Corridor] | 10 | 1 | 20-Jun-14 A | 16-Jul-14 | 21 |
| L1B-6012 | Fire Sprinkler RI [including East Service Corridor] | 10 | 1 | 21-Jun-14 A | 16-Jul-14 | 21 |
| L1L-6018 | HVAC RI [including back of house] | 10 | 8 | 23-Jun-14 A | 04-Aug-14 | 4 |
| L1L-6014 | Plumbing RI [including back of house] | 10 | 8 | 24-Jun-14 A | 04-Aug-14 | 4 |
| L1L-6012 | Fire Sprinkler RI [including back of house] | 10 | 8 | 25-Jun-14 A | 04-Aug-14 | 4 |
| L1L-6016 | Electrical RI [including back of house] | 10 | 8 | 25-Jun-14 A | 04-Aug-14 | 4 |
| L1L-6022 | Fire Alarm / Elec Specialties RI [including back of hou | 10 | 9 | 27-Jun-14 A | 05-Aug-14 | 12 |
| L1K-6022 | Fire Alarm / Elec Specialties RI [including public restro | 10 | 9 | 27-Jun-14 A | 29-Jul-14 | 8 |

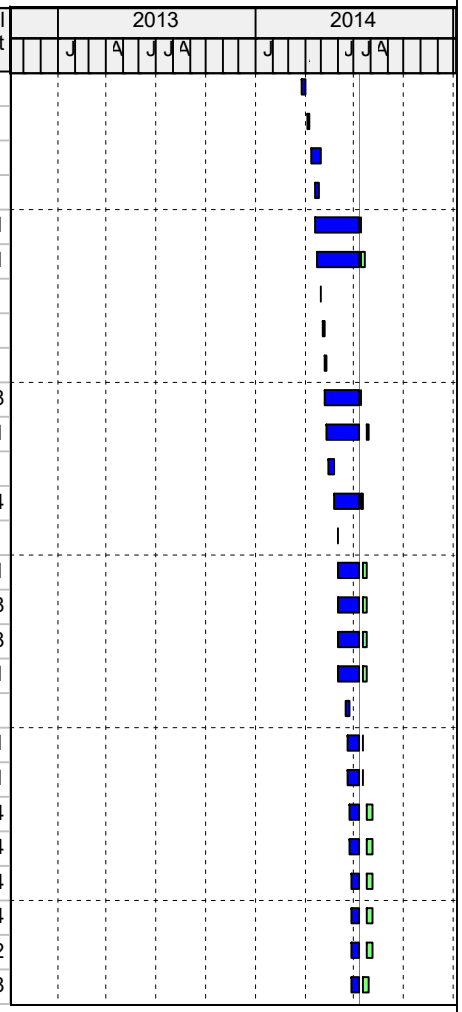


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-6016 | Electrical RI [including East Service Corridor] | 10 | 5 | 07-Jul-14 A | 22-Jul-14 | 22 |
| L1B-6022 | Fire Alarm / Elec Specialties RI [including East Service | 10 | 5 | 07-Jul-14 A | 22-Jul-14 | 22 |
| LL1-6010 | CMU Seismic Clips | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 25 |
| LL1-Z2-6010 | CMU Seismic Clips | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 113 |
| L1B-6010 | CMU Seismic Clips [including East Service Corridor] | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 113 |
| L1L-6010 | CMU Seismic Clips [including back of house] | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 9 |
| L1K-6010 | CMU Seismic Clips [including public restroom] | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 113 |
| LL1-Z3-6010 | CMU Seismic Clips (At All Areas North of Q-Line) | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 112 |
| L1B-6009 | Frame Ceilings [including East Service Corridor] | 10 | 10 | 17-Jul-14 | 30-Jul-14 | 21 |
| LL1-Z2-6009 | Frame Ceilings | 10 | 10 | 18-Jul-14 | 31-Jul-14 | 15 |
| LL1-Z3-6009 | Frame Ceilings (At All Areas North of Q-Line) | 3 | 3 | 25-Jul-14 | 29-Jul-14 | 17 |
| LL1-Z3C-6012 | Complete Fire Sprinkler RI @ Ceilings (At All Areas Nc | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 27 |
| LL1-Z3C-6014 | Complete Plumbing RI @ Ceilings (At All Areas North | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 17 |
| L1K-6009 | Frame Ceilings [including public restroom] | 10 | 10 | 30-Jul-14 | 12-Aug-14 | 8 |
| LL1-6024 | Inspections for Cover | 2 | 2 | 31-Jul-14 | 01-Aug-14 | 21 |
| L1B-6020 | Hollow Metal Door Frames [including East Service Co | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 23 |
| L1BC-6012 | Complete Fire Sprinkler RI @ Ceilings [including East | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 23 |
| L1BC-6014 | Complete Plumbing RI @ Ceilings [including East Se | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 21 |
| L1BC-6016 | Complete Electrical RI @ Ceilings [including East Ser | 7 | 7 | 31-Jul-14 | 08-Aug-14 | 21 |
| L1BC-6018 | Complete HVAC RI @ Ceilings [including East Service | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 23 |
| L1BC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings \| | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 23 |
| LL1-Z2-6024 | Inspections for Cover | 2 | 2 | 05-Aug-14 | 06-Aug-14 | 15 |
| L1L-6009 | Frame Ceilings [including back of house] | 10 | 10 | 05-Aug-14 | 18-Aug-14 | 4 |
| LL1-Z3C-6016 | Complete Electrical RI @ Ceilings (At All Areas North ( | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 17 |
| LL1-Z3C-6018 | Complete HVAC RI @ Ceilings (At All Areas North of ( | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 22 |
| L1B-6024 | Inspections for Cover [including East Service Corridor] | 2 | 2 | 11-Aug-14 | 12-Aug-14 | 21 |
| LL1-Z3C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings ( | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 17 |

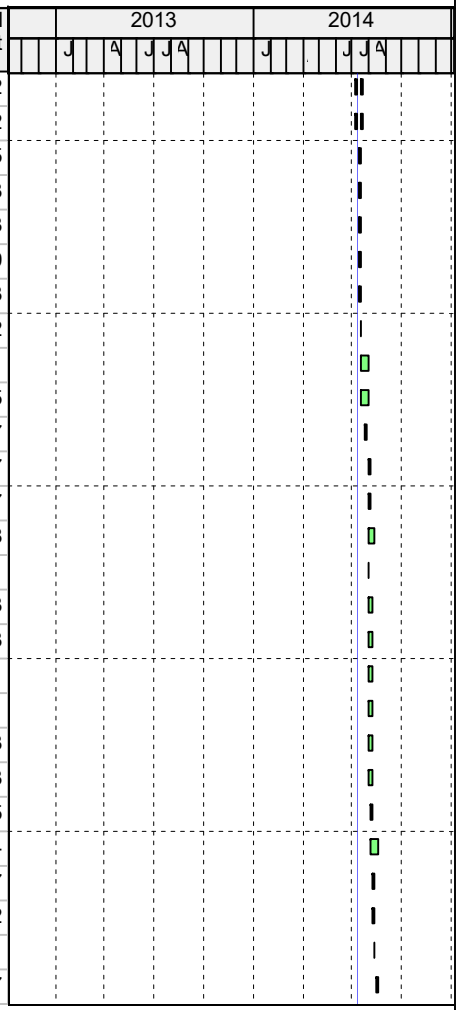


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-6020 | Hollow Metal Door Frames [including public restroom] | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 18 |
| L1KC-6012 | Complete Fire Sprinkler RI @ Ceilings [including publi | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 18 |
| L1KC-6014 | Complete Plumbing RI @ Ceilings [including public re | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 8 |
| L1L-6020 | Hollow Metal Door Frames [including back of house] | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 9 |
| L1LC-6012 | Complete Fire Sprinkler RI @ Ceilings [including back | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 9 |
| L1LC-6014 | Complete Plumbing RI @ Ceilings [including back of I | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 4 |
| L1LC-6016 | Complete Electrical RI @ Ceilings [including back of h | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 4 |
| LL1-Z3-6024 | Inspections for Cover (At All Areas North of Q-Line) | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 17 |
| L1KC-6016 | Complete Electrical RI @ Ceilings [including public res | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 8 |
| L1KC-6018 | Complete HVAC RI @ Ceilings [including public restro | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 13 |
| L1LC-6018 | Complete HVAC RI @ Ceilings [including back of hou | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 4 |
| L1LC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 4 |
| L1KC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 8 |
| L1L-6024 | Inspections for Cover [including back of house] | 2 | 2 | 03-Sep-14 | 04-Sep-14 | 4 |
| L1K-6024 | Inspections for Cover [including public restroom] | 2 | 2 | 04-Sep-14 | 05-Sep-14 | 8 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 0 | 17-Apr-14 A | 09-May-14 A | |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6006 | L2 - Support Frame/Sheathing for Metal Panels | 6 | 6 | 23-Apr-14 A | 21-Jul-14 | 25 |
| L02-6008 | L2 - Int Wall Framing | 10 | 2 | 25-Apr-14 A | 23-Jul-14 | 25 |
| L02-6014 | L2 - Plumbing RI | 15 | 2 | 28-Apr-14 A | 25-Jul-14 | 25 |
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 0 | 28-Apr-14 A | 09-May-14 A | |
| L02-6004 | L2 - CMU Walls | 5 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L02-6002 | L2 - Layout | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L02-6018 | L2 - HVAC RI (including equipment) | 20 | 8 | 18-Jun-14 A | 04-Aug-14 | 27 |
| L02-6016 | L2 - Electrical RI | 10 | 8 | 24-Jun-14 A | 04-Aug-14 | 25 |

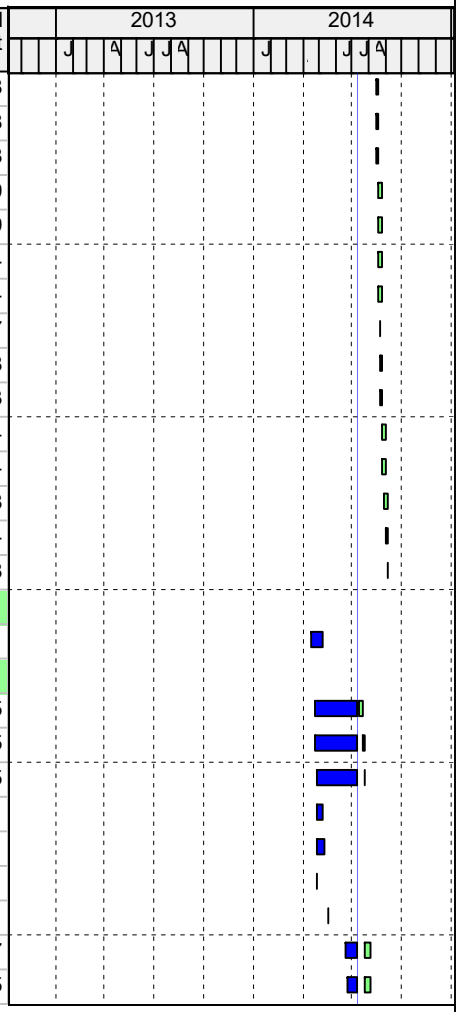


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-6012 | L2 - Fire Sprinkler RI | 10 | 7 | 26-Jun-14 A | 01-Aug-14 | 28 |
| L02-6020 | L2 - H Mtl Frames | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 30 |
| L02-6022 | L2 - Fire Alarm / Elec Specialties RI | 10 | 10 | 24-Jul-14 | 06-Aug-14 | 25 |
| L02-6024 | L2 - Inspections | 2 | 2 | 07-Aug-14 | 08-Aug-14 | 25 |
| Upper Tower - (Levels 3 thru PH) | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L07-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 01-Apr-11 A | 11-Apr-11 A | |
| L04-6012 | Fire Sprinkler Mains | 5 | 0 | 01-Feb-14 A | 03-Apr-14 A | |
| L03-8219 | HVAC Risers | 5 | 0 | 11-Feb-14 A | 23-Mar-14 A | |
| L03-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 11-Feb-14 A | 03-Mar-14 A | |
| L03-6002 | Layout | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| L04-8219 | HVAC Risers | 5 | 0 | 13-Feb-14 A | 23-Mar-14 A | |
| L05-8219 | HVAC Risers | 5 | 0 | 17-Feb-14 A | 03-Mar-14 A | |
| L03-6008 | Frame Shaft Walls | 3 | 0 | 18-Feb-14 A | 26-Mar-14 A | |
| L04-6002 | Layout | 5 | 0 | 19-Feb-14 A | 25-Feb-14 A | |
| L04-6008 | Frame Shaft Walls | 3 | 0 | 20-Feb-14 A | 26-Mar-14 A | |
| L03-6011 | PreRock Shafts | 2 | 0 | 24-Feb-14 A | 25-Mar-14 A | |
| L03-6010 | Frame Walls | 5 | 0 | 25-Feb-14 A | 25-Mar-14 A | |
| L05-6002 | Layout | 5 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| L04-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 28-Feb-14 A | 05-Mar-14 A | |
| L03-6016 | Electrical RI | 5 | 0 | 03-Mar-14 A | 04-Apr-14 A | |
| L03-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 12-Mar-14 A | |
| L04-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 13-Mar-14 A | |
| L04-6010 | Frame Walls | 5 | 0 | 04-Mar-14 A | 05-Jun-14 A | |
| L05-6008 | Frame Shaft Walls | 3 | 0 | 05-Mar-14 A | 27-Mar-14 A | |
| L06-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L07-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |

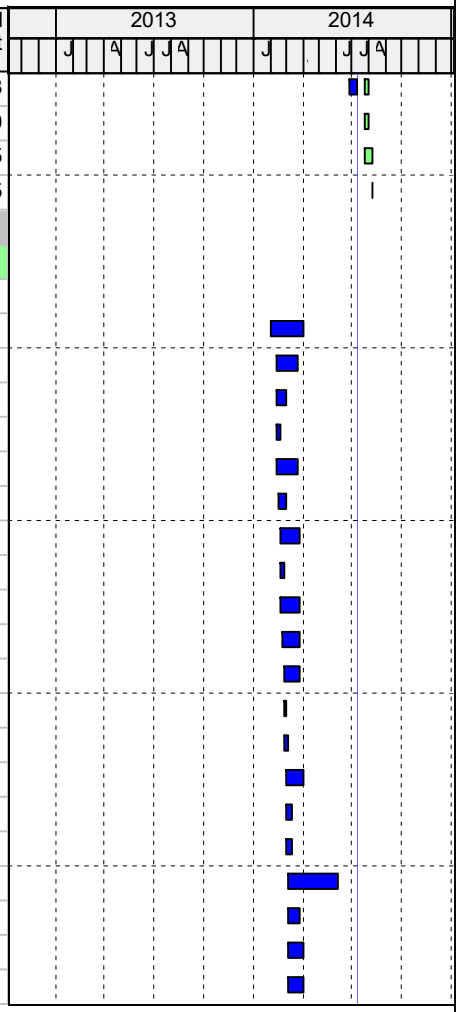



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 06-Mar-14 A | 21-Mar-14 A | |
| L03-6020 | Install Hollow Metal Frames | 3 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L04-6020 | Install Hollow Metal Frames | 3 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L05-6010 | Frame Walls | 5 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L06-6002 | Layout | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L04-6011 | PreRock Shafts | 2 | 0 | 18-Mar-14 A | 25-Mar-14 A | |
| L05-6009 | Inspect Shafts | 1 | 0 | 18-Mar-14 A | 18-Mar-14 A | |
| L05-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| L06-6008 | Frame Shaft Walls | 3 | 0 | 19-Mar-14 A | 03-Apr-14 A | |
| L06-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 27-Mar-14 A | |
| L04-6016 | Electrical RI | 5 | 0 | 20-Mar-14 A | 09-Apr-14 A | |
| L05-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 26-Mar-14 A | |
| L06-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 07-Apr-14 A | |
| L07-6002 | Layout | 5 | 0 | 24-Mar-14 A | 30-Apr-14 A | |
| L03-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L03-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L05-6016 | Electrical RI | 5 | 0 | 25-Mar-14 A | 05-Jun-14 A | |
| L04-6019 | Complete Top Out GWB | 2 | 0 | 26-Mar-14 A | 06-Jun-14 A | |
| L05-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L06-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| L03-6019 | Complete Top Out GWB | 2 | 0 | 27-Mar-14 A | 02-May-14 A | |
| L08-6002 | Layout | 5 | 0 | 27-Mar-14 A | 02-Apr-14 A | |
| L05-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 28-Mar-14 A | 03-Apr-14 A | |
| L06-6010 | Frame Walls | 5 | 0 | 28-Mar-14 A | 07-Apr-14 A | |
| L03-6012 | Fire Sprinkler Mains | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |

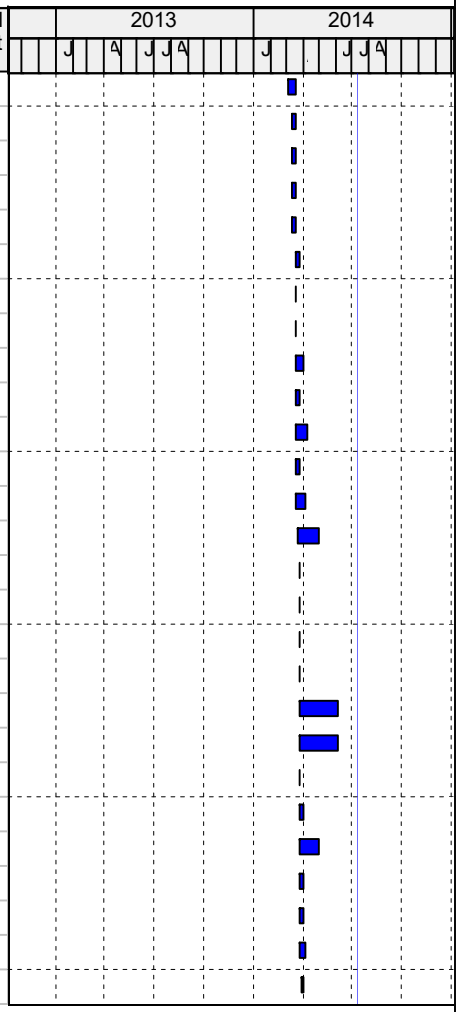



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6008 | Frame Shaft Walls | 3 | 0 | 31-Mar-14 A | 03-Apr-14 A | |
| L05-6019 | Complete Top Out GWB | 2 | 0 | 01-Apr-14 A | 08-Apr-14 A | |
| L08-6008 | Frame Shaft Walls | 3 | 0 | 02-Apr-14 A | 21-Apr-14 A | |
| L03-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L04-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L05-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L06-6016 | Electrical RI | 5 | 0 | 03-Apr-14 A | 15-Apr-14 A | |
| L07-6009 | Inspect Shafts | 1 | 0 | 03-Apr-14 A | 03-Apr-14 A | |
| L07-6011 | PreRock Shafts | 2 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| L05-6012 | Fire Sprinkler Mains | 5 | 0 | 04-Apr-14 A | 30-Apr-14 A | |
| L06-6012 | Fire Sprinkler Mains | 5 | 0 | 07-Apr-14 A | 30-Apr-14 A | |
| L06-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L06-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L07-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| L07-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L03-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L03-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L04-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L06-6009 | Inspect Shafts | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L06-6019 | Complete Top Out GWB | 2 | 0 | 08-Apr-14 A | 18-Apr-14 A | |
| L07-6010 | Frame Walls | 5 | 0 | 08-Apr-14 A | 15-Apr-14 A | |
| L08-6011 | PreRock Shafts | 2 | 0 | 08-Apr-14 A | 23-Apr-14 A | |
| L09-6002 | Layout | 5 | 0 | 08-Apr-14 A | 26-Apr-14 A | |
| L03-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 09-Apr-14 A | 08-May-14 A | |
| L03-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L05-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 09-Apr-14 A | 14-Apr-14 A | |
| L08-6009 | Inspect Shafts | 1 | 0 | 09-Apr-14 A | 25-Apr-14 A | |

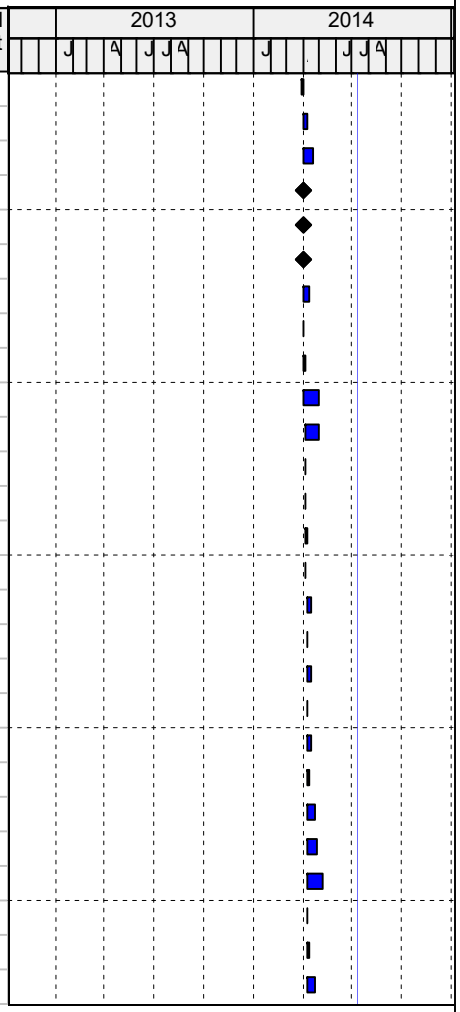



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6008 | Frame Shaft Walls | 3 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| L08-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| L04-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 15-Apr-14 A | 16-Apr-14 A | |
| L07-6012 | Fire Sprinkler Mains | 5 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| L07-6016 | Electrical RI | 5 | 0 | 15-Apr-14 A | 12-May-14 A | |
| L07-6020 | Install Hollow Metal Frames | 3 | 0 | 16-Apr-14 A | 23-Apr-14 A | |
| L05-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 17-Apr-14 A | 25-Apr-14 A | |
| L06-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 17-Apr-14 A | 12-May-14 A | |
| L06-6023 | Inspection of Exterior Framing | 0 | 0 | 17-Apr-14 A | | |
| L09-8219 | HVAC Risers | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L09-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L04-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 18-Apr-14 A | 20-Apr-14 A | |
| L04-6028 | PreRock at Heat Pumps | 2 | 0 | 20-Apr-14 A | 22-Apr-14 A | |
| L08-8219 | HVAC Risers | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6009 | Inspect Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6011 | PreRock Shafts | 2 | 0 | 22-Apr-14 A | 24-Apr-14 A | |
| L04-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L06-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 23-Apr-14 A | 25-Apr-14 A | |
| L08-6020 | Install Hollow Metal Frames | 3 | 0 | 23-Apr-14 A | 13-May-14 A | |
| L11-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L11-8220 | Plumbing Risers - Install | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L04-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L09-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L10-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L10-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 20-May-14 A | |

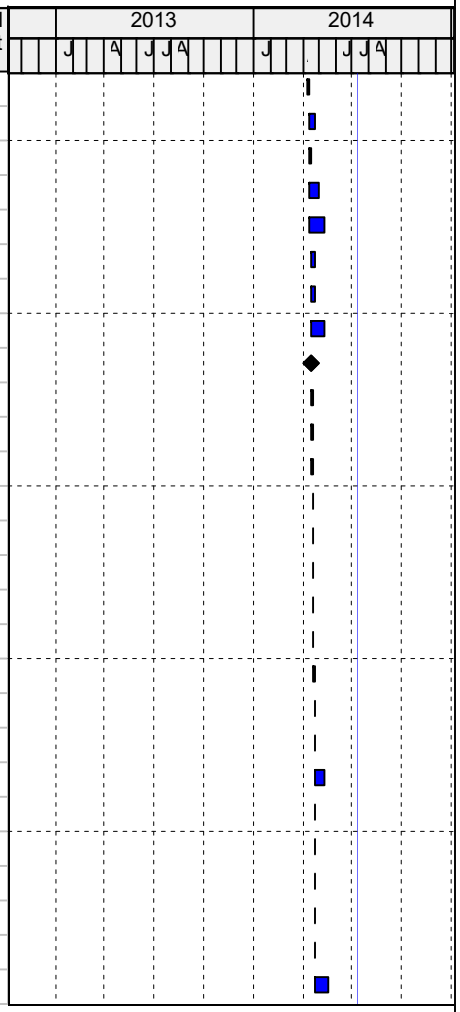



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L04-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 25-Apr-14 A | 11-Jun-14 A | |
| L04-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L09-6010 | Frame Walls | 5 | 0 | 25-Apr-14 A | 20-May-14 A | |
| L09-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L10-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L11-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 30-Apr-14 A | |
| L12-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L08-6010 | Frame Walls | 5 | 0 | 26-Apr-14 A | 30-Apr-14 A | |
| L10-6002 | Layout | 5 | 0 | 27-Apr-14 A | 27-Apr-14 A | |
| L04-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 28-Apr-14 A | 30-Apr-14 A | |
| L05-6018 | HVAC RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6028 | PreRock at Heat Pumps | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L07-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 28-Apr-14 A | 12-May-14 A | |
| L10-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-Apr-14 A | 22-May-14 A | |
| L11-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L12-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L05-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| L05-6028 | PreRock at Heat Pumps | 2 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L06-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 09-May-14 A | |
| L06-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |

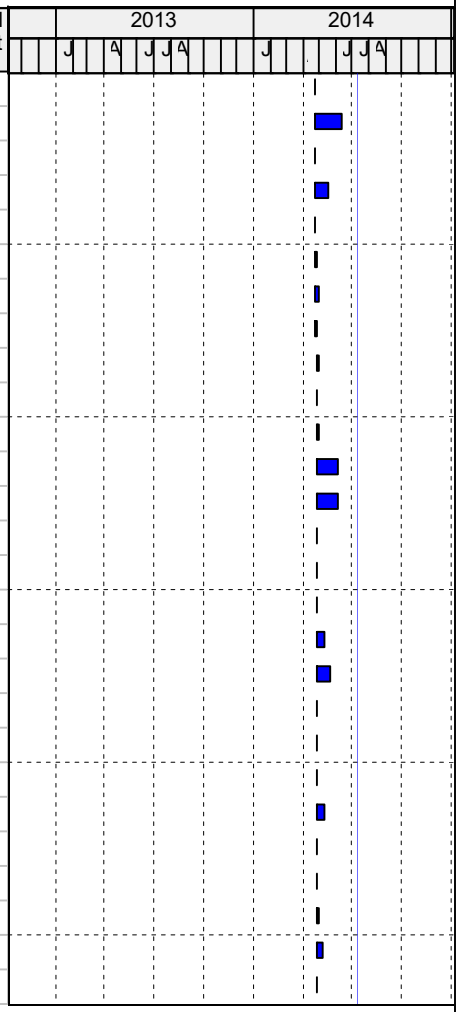



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L08-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L08-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L09-6020 | Install Hollow Metal Frames | 3 | 0 | 29-Apr-14 A | 20-May-14 A | |
| L09-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L10-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L04-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 30-Apr-14 A | 02-May-14 A | |
| L09-6019 | Complete Top Out GWB | 2 | 0 | 30-Apr-14 A | 06-Jun-14 A | |
| L11-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L12-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L03-6028 | PreRock at Heat Pumps | 2 | 0 | 01-May-14 A | 02-May-14 A | |
| L05-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L06-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L03-6014 | Set Tubs & Plumbing RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L05-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L05-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| L06-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L06-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 09-May-14 A | |
| L03-6018 | HVAC RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L03-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 06-May-14 A | 06-May-14 A | |
| L07-6014 | Set Tubs & Plumbing RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L07-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 06-May-14 A | 09-May-14 A | |
| L03-6004 | CMU Wall/Clips | 3 | 0 | 07-May-14 A | 08-May-14 A | |

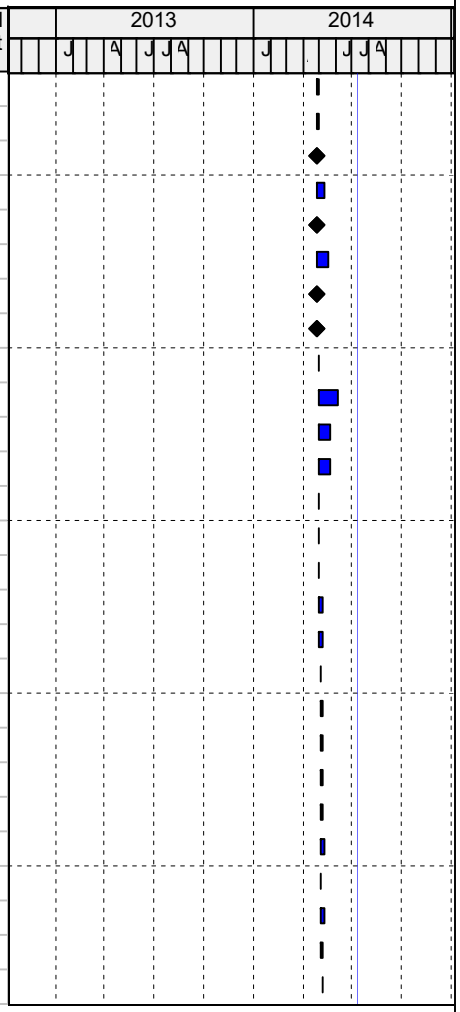



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L03-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 08-May-14 A | 13-May-14 A | |
| L03-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6004 | CMU Walls | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6018 | HVAC RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L11-6010 | Frame Walls | 5 | 0 | 09-May-14 A | 15-May-14 A | |
| L05-6014 | Set Tubs & Plumbing RI | 5 | 0 | 12-May-14 A | 05-Jun-14 A | |
| L07-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 12-May-14 A | 13-May-14 A | |
| L11-6020 | Install Hollow Metal Frames | 3 | 0 | 12-May-14 A | 14-May-14 A | |
| L11-6019 | Complete Top Out GWB | 2 | 0 | 12-May-14 A | 14-May-14 A | |
| L14-6002 | Layout | 5 | 0 | 12-May-14 A | 14-May-14 A | |
| L15-6002 | Layout | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L05-6004 | CMU Walls | 3 | 0 | 13-May-14 A | 13-May-14 A | |
| L06-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 25-Jun-14 A | |
| L06-6022 | Fire Alarm / Elec Specialties RI | 5 | 1 | 13-May-14 A | 14-Jul-14 | 4 |
| L07-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 05-Jun-14 A | |
| L07-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| L07-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 13-May-14 A | 13-May-14 A | |
| L14-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L16-6002 | Layout | 5 | 0 | 13-May-14 A | 16-May-14 A | |
| L06-6004 | CMU Walls | 3 | 0 | 14-May-14 A | 14-May-14 A | |
| L07-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 15-May-14 A | |
| L08-6012 | Fire Sprinkler Mains | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 20-May-14 A | |

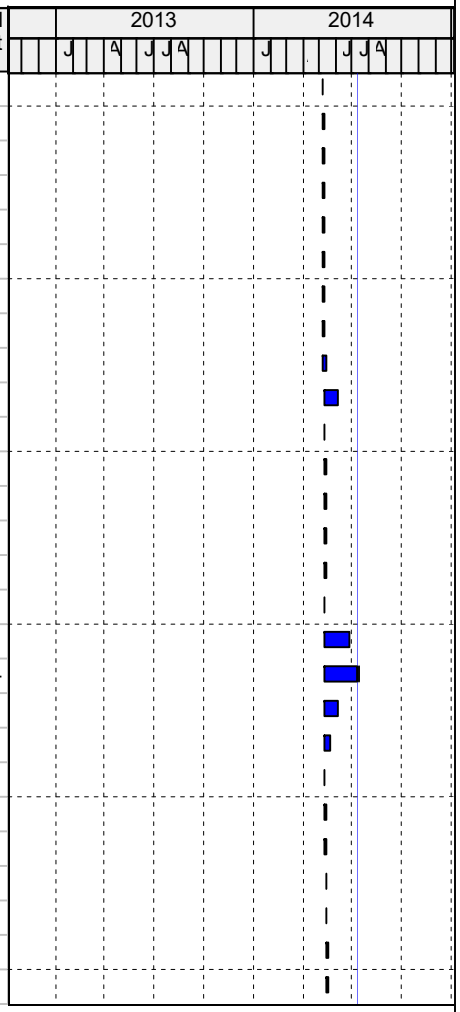



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6002 | Layout | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L07-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6014 | Set Tubs & Plumbing RI | 5 | 0 | 16-May-14 A | 25-Jun-14 A | |
| L08-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L11-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L12-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L07-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L08-6028 | PreRock at Heat Pumps | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L09-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L10-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L11-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L15-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 19-May-14 A | 19-May-14 A | |
| L07-6028 | PreRock at Heat Pumps | 2 | 0 | 20-May-14 A | 21-May-14 A | |
| L07-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L08-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 20-May-14 A | 21-May-14 A | |
| L10-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L11-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L14-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L07-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 21-May-14 A | 27-May-14 A | |
| L08-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L08-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L09-6028 | PreRock at Heat Pumps | 2 | 0 | 21-May-14 A | 22-May-14 A | |

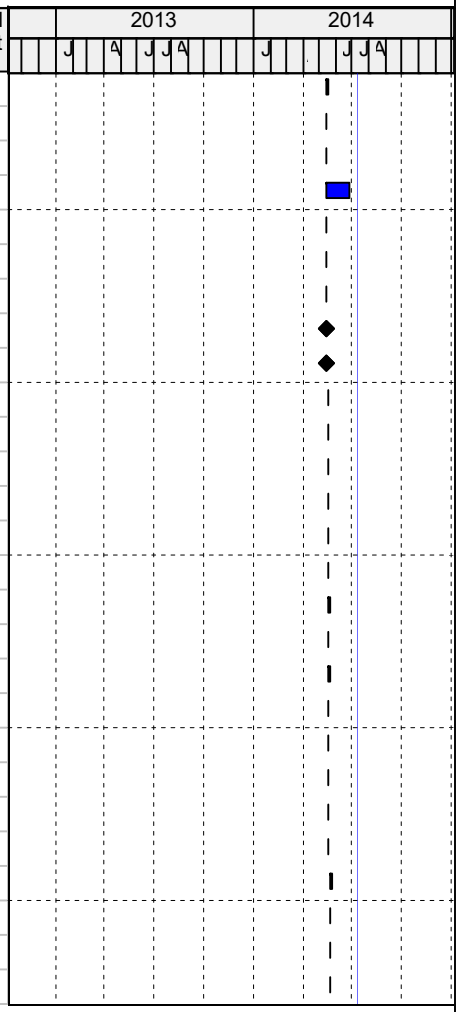



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 21-May-14 A | 27-Jun-14 A | |
| L10-6010 | Frame Walls | 5 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6019 | Complete Top Out GWB | 2 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L11-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L12-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L14-8220 | Plumbing Risers - Install | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L15-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L16-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L07-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| L08-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 22-May-14 A | 22-May-14 A | |
| L10-6012 | Fire Sprinkler Mains | 5 | 0 | 22-May-14 A | 27-May-14 A | |
| L08-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L09-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6020 | Install Hollow Metal Frames | 3 | 0 | 23-May-14 A | 03-Jun-14 A | |
| L10-6028 | PreRock at Heat Pumps | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L14-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L15-8220 | Plumbing Risers - Install | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L09-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 27-May-14 A | 27-May-14 A | |
| L12-6010 | Frame Walls | 5 | 0 | 27-May-14 A | 02-Jun-14 A | |
| L08-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L09-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 28-May-14 A | 28-May-14 A | |
| L10-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 28-May-14 A | 03-Jun-14 A | |
| L14-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L15-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-May-14 A | 30-May-14 A | |
| L16-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 28-May-14 A | 28-May-14 A | |
| L16-8220 | Plumbing Risers - Install | 2 | 0 | 28-May-14 A | 29-May-14 A | |

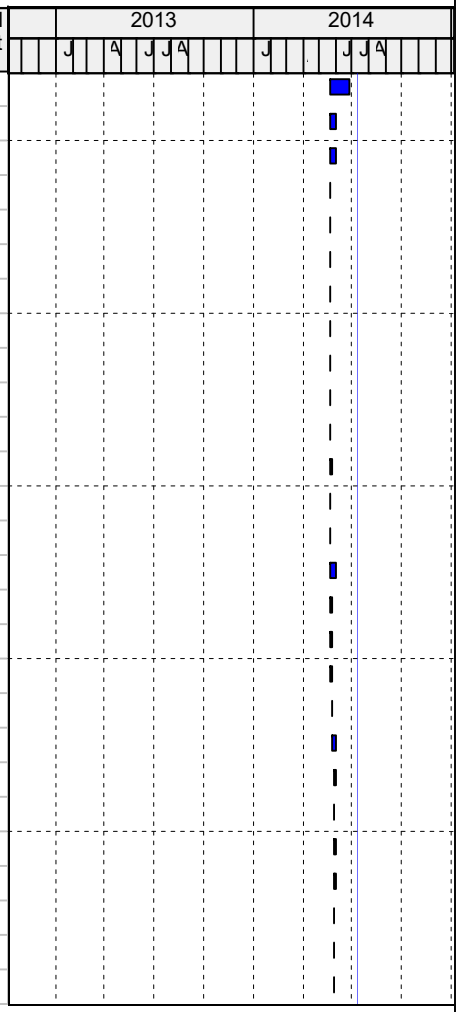



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 29-May-14 A | 30-May-14 A | |
| L10-6016 | Electrical RI | 5 | 1 | 29-May-14 A | 17-Jul-14 | 11 |
| L10-6022 | Fire Alarm / Elec Specialties RI | 4 | 2 | 29-May-14 A | 18-Jul-14 | 11 |
| L10-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L10-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| L12-6012 | Fire Sprinkler Mains | 5 | 0 | 30-May-14 A | 26-Jun-14 A | |
| L12-6020 | Install Hollow Metal Frames | 3 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L15-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L17-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L17-8220 | Plumbing Risers - Install | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L10-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L11-6016 | Electrical RI | 5 | 4 | 02-Jun-14 A | 23-Jul-14 | 12 |
| L11-6022 | Fire Alarm / Elec Specialties RI | 4 | 4 | 02-Jun-14 A | 24-Jul-14 | 11 |
| L12-6019 | Complete Top Out GWB | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L14-6020 | Install Hollow Metal Frames | 3 | 0 | 02-Jun-14 A | 05-Jun-14 A | |
| L14-6010 | Frame Walls | 5 | 0 | 02-Jun-14 A | 04-Jun-14 A | |
| L16-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| L14-6019 | Complete Top Out GWB | 2 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L16-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L10-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| L17-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 04-Jun-14 A | 11-Jun-14 A | |
| L08-6016 | Electrical RI | 5 | 1 | 05-Jun-14 A | 14-Jul-14 | 11 |
| L08-6022 | Fire Alarm / Elec Specialties RI | 5 | 1 | 05-Jun-14 A | 14-Jul-14 | 11 |
| L09-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L12-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L15-6010 | Frame Walls | 3 | 0 | 05-Jun-14 A | 11-Jun-14 A | |
| L09-6012 | Fire Sprinkler Mains | 5 | 0 | 06-Jun-14 A | 09-Jun-14 A | |

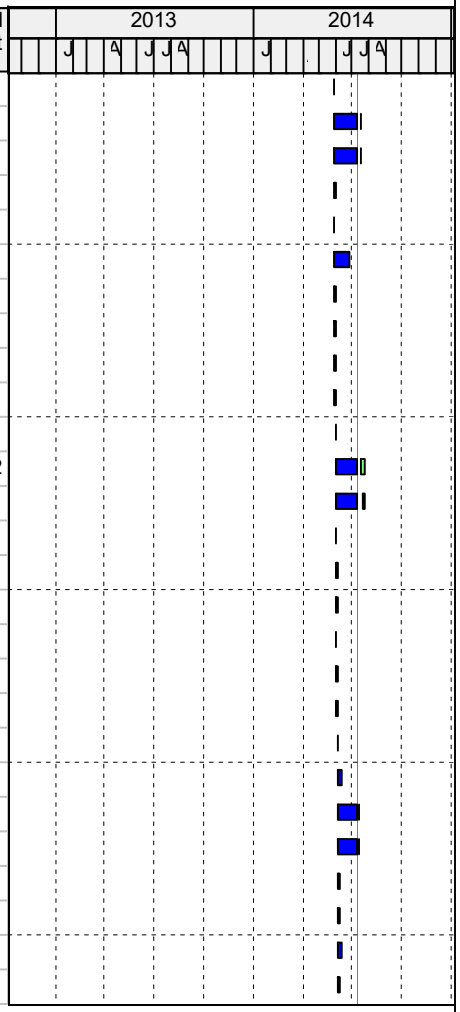



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L11-6012 | Fire Sprinkler Mains | 4 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L12-6014 | Set Tubs & Plumbing RI | 4 | 0 | 06-Jun-14 A | 27-Jun-14 A | |
| L11-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jun-14 A | 11-Jun-14 A | |
| L09-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-Jun-14 A | 25-Jun-14 A | |
| L14-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L15-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L16-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L09-6016 | Electrical RI | 5 | 2 | 10-Jun-14 A | 16-Jul-14 | 11 |
| L09-6022 | Fire Alarm / Elec Specialties RI | 5 | 2 | 10-Jun-14 A | 16-Jul-14 | 11 |
| L09-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L14-6014 | Set Tubs & Plumbing RI | 4 | 1 | 10-Jun-14 A | 14-Jul-14 | 23 |
| L15-6020 | Install Hollow Metal Frames | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L15-6019 | Complete Top Out GWB | 2 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6014 | Set Tubs & Plumbing RI | 4 | 0 | 11-Jun-14 A | 26-Jun-14 A | |
| L11-6028 | PreRock at Heat Pumps | 2 | 0 | 13-Jun-14 A | 14-Jun-14 A | |
| L11-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 14-Jun-14 A | 14-Jun-14 A | |
| L14-6012 | Fire Sprinkler Mains | 2 | 0 | 16-Jun-14 A | 27-Jun-14 A | |
| L14-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 0 | 18-Jun-14 A | 18-Jun-14 A | |
| L15-6023 | Inspection of Exterior Framing | 0 | 0 | 18-Jun-14 A | | |
| L17-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 18-Jun-14 A | 23-Jun-14 A | |
| L17-6010 | Frame Walls | 5 | 1 | 18-Jun-14 A | 15-Aug-14 | 10 |
| L10-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L12-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 19-Jun-14 A | |

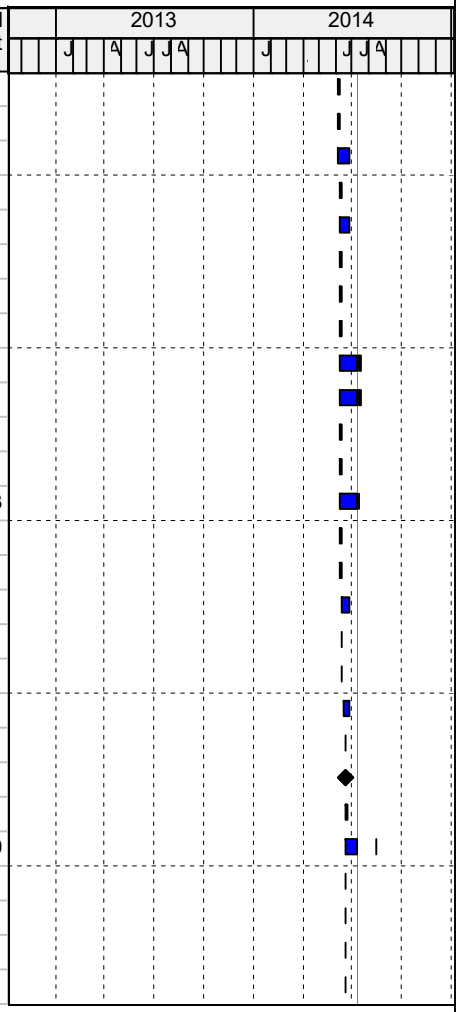



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6023 | Inspection of Exterior Framing | 0 | 0 | 20-Jun-14 A | | |
| L15-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-Jun-14 A | 20-Jun-14 A | |
| L10-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-Jun-14 A | 23-Jun-14 A | |
| L15-6014 | Set Tubs & Plumbing Rl | 5 | 4 | 22-Jun-14 A | 14-Aug-14 | 4 |
| L08-6018 | HVAC Rl | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L12-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L14-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L15-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L08-6221 | Frame Unit Ceilings | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| L11-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 24-Jun-14 A | 27-Jun-14 A | |
| L12-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L14-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6023 | Inspection of Exterior Framing | 0 | 0 | 24-Jun-14 A | | |
| L12-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| L12-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L14-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L15-6012 | Fire Sprinkler Mains | 2 | 1 | 25-Jun-14 A | 11-Aug-14 | 7 |
| L16-6023 | Inspection of Exterior Framing | 0 | 0 | 25-Jun-14 A | | |
| L03-6024 | Inspections for GWB Cover | 1 | 0 | 27-Jun-14 A | 27-Jun-14 A | |
| L09-6018 | HVAC Rl | 3 | 1 | 27-Jun-14 A | 14-Jul-14 | 15 |
| L09-6221 | Frame Unit Ceilings | 2 | 0 | 27-Jun-14 A | 30-Jun-14 A | |
| L12-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L14-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L15-6028 | PreRock at Heat Pumps | 2 | 0 | 30-Jun-14 A | 01-Jul-14 A | |
| L16-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 30-Jun-14 A | 30-Jun-14 A | |
| L16-6010 | Frame Walls | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |

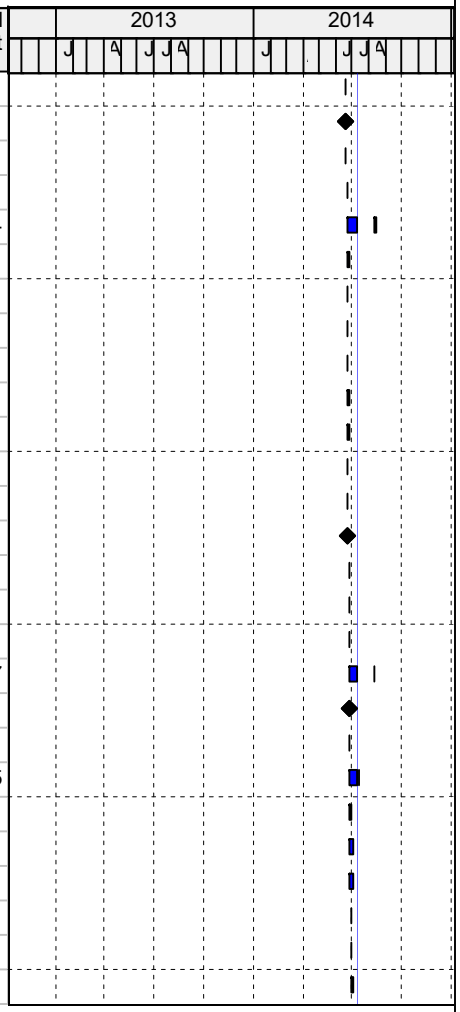



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L15-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L15-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L04-6024 | Inspections for GWB Cover | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L10-6018 | HVAC RI | 3 | 1 | 07-Jul-14 A | 14-Jul-14 | 18 |
| L11-6221 | Frame Unit Ceilings | 2 | 0 | 07-Jul-14 A | 14-Jul-14 | 18 |
| L11-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L15-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L16-6012 | Fire Sprinkler Mains | 2 | 2 | 07-Jul-14 A | 18-Aug-14 | 11 |
| L16-6020 | Install Hollow Metal Frames | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L16-6028 | PreRock at Heat Pumps | 2 | 1 | 07-Jul-14 A | 14-Jul-14 | 25 |
| L17-6019 | Complete Top Out GWB | 1 | 1 | 07-Jul-14 A | 18-Aug-14 | 15 |
| L03-6000 | Skim Ceiling/Tape GWB | 6 | 2 | 08-Jul-14 A | 16-Jul-14 | 57 |
| L11-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L15-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 2 | 08-Jul-14 A | 15-Jul-14 | 21 |
| L17-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 1 | 08-Jul-14 A | 15-Jul-14 | 38 |
| L10-6221 | Frame Unit Ceilings | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| L17-6012 | Fire Sprinkler Mains | 2 | 2 | 09-Jul-14 A | 20-Aug-14 | 13 |
| L05-6024 | Inspections for GWB Cover | 1 | 0 | 10-Jul-14 A | 10-Jul-14 A | |
| L04-6000 | Skim Ceiling/Tape GWB | 6 | 4 | 11-Jul-14 A | 21-Jul-14 | 54 |
| L11-6018 | HVAC RI | 3 | 3 | 14-Jul-14 | 16-Jul-14 | 21 |
| L11-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 21 |
| L12-6221 | Frame Unit Ceilings | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 19 |
| L12-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 24 |
| L14-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 27 |
| L15-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 31 |
| L06-6024 | Inspections for GWB Cover | 1 | 1 | 15-Jul-14 | 15-Jul-14 | 4 |

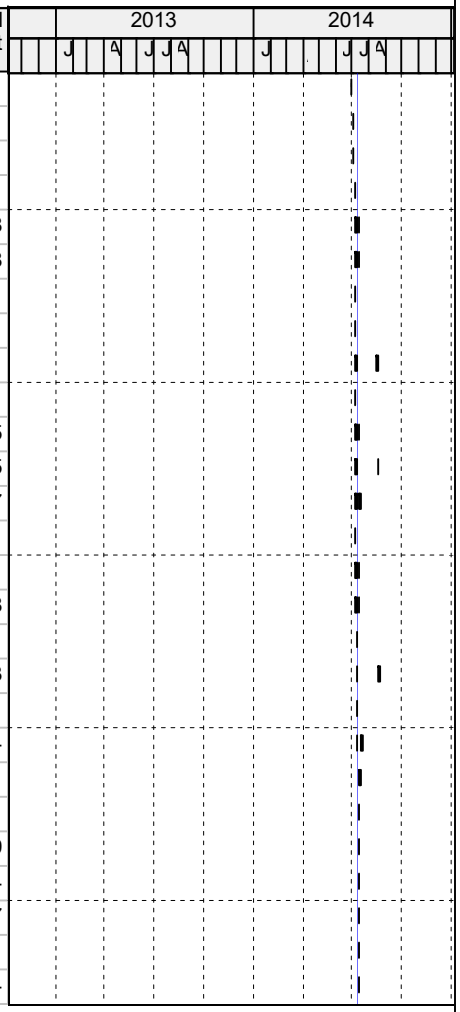


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6221 | Frame Unit Ceilings | 2 | 2 | 15-Jul-14 | 16-Jul-14 | 23 |
| L16-6029 | Inspection of PreRock at Heat Pumps | 1 | 1 | 15-Jul-14 | 15-Jul-14 | 25 |
| L16-6030 | Tape/Firecaulk at Heat Pumps | 1 | 1 | 16-Jul-14 | 16-Jul-14 | 25 |
| L12-6018 | HVAC RI | 3 | 3 | 17-Jul-14 | 21-Jul-14 | 21 |
| L16-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 1 | 17-Jul-14 | 17-Jul-14 | 25 |
| L16-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 3 | 18-Jul-14 | 22-Jul-14 | 25 |
| L07-6024 | Inspections for GWB Cover | 1 | 1 | 21-Jul-14 | 21-Jul-14 | 4 |
| L16-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 21-Jul-14 | 22-Jul-14 | 30 |
| L05-6000 | Skim Ceiling/Tape GWB | 6 | 6 | 22-Jul-14 | 29-Jul-14 | 48 |
| L14-6018 | HVAC RI | 3 | 3 | 22-Jul-14 | 24-Jul-14 | 22 |
| L12-6016 | Electrical RI | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 12 |
| L08-6024 | Inspections for GWB Cover | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 4 |
| L12-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 25-Jul-14 | 31-Jul-14 | 11 |
| L17-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 1 | 25-Jul-14 | 25-Jul-14 | 16 |
| L06-6000 | Skim Ceiling/Tape GWB | 6 | 6 | 28-Jul-14 | 04-Aug-14 | 60 |
| L17-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 1 | 28-Jul-14 | 28-Jul-14 | 16 |
| L17-6028 | PreRock at Heat Pumps | 2 | 2 | 29-Jul-14 | 30-Jul-14 | 16 |
| L09-6024 | Inspections for GWB Cover | 1 | 1 | 31-Jul-14 | 31-Jul-14 | 4 |
| L14-6016 | Electrical RI | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 12 |
| L17-6029 | Inspection of PreRock at Heat Pumps | 1 | 1 | 31-Jul-14 | 31-Jul-14 | 16 |
| L07-6000 | Skim Ceiling/Tape GWB | 6 | 6 | 01-Aug-14 | 08-Aug-14 | 56 |
| L14-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 01-Aug-14 | 07-Aug-14 | 11 |
| L17-6030 | Tape/Firecaulk at Heat Pumps | 1 | 1 | 01-Aug-14 | 01-Aug-14 | 16 |
| L17-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 1 | 04-Aug-14 | 04-Aug-14 | 16 |
| L17-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 3 | 05-Aug-14 | 07-Aug-14 | 16 |
| L10-6024 | Inspections for GWB Cover | 1 | 1 | 06-Aug-14 | 06-Aug-14 | 4 |
| L17-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 06-Aug-14 | 07-Aug-14 | 22 |

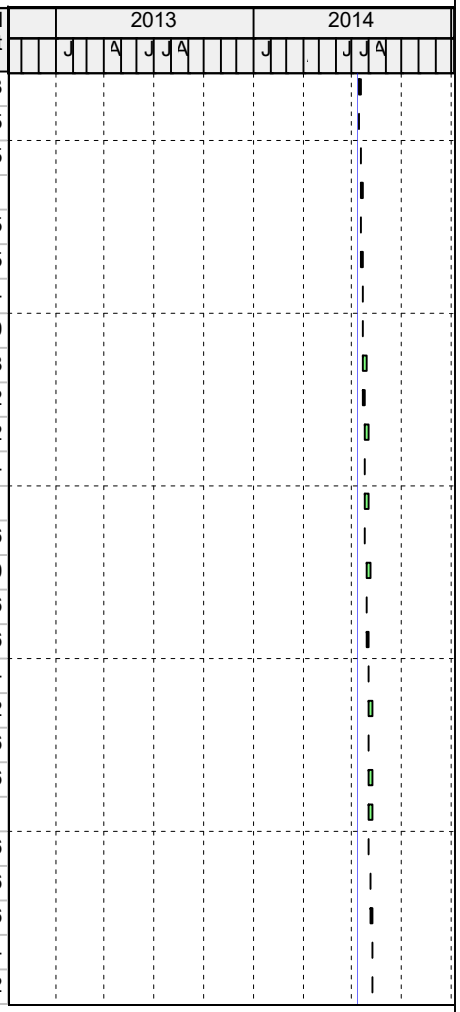



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-6000 | Skim Ceiling/Tape GWB | 6 | 6 | 07-Aug-14 | 14-Aug-14 | 52 |
| L11-6024 | Inspections for GWB Cover | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 4 |
| L09-6000 | Skim Ceiling/Tape GWB | 6 | 6 | 13-Aug-14 | 20-Aug-14 | 48 |
| L15-6221 | Frame Unit Ceilings | 2 | 2 | 15-Aug-14 | 18-Aug-14 | 4 |
| L16-6014 | Set Tubs & Plumbing RI | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 6 |
| L16-6019 | Complete Top Out GWB | 1 | 1 | 15-Aug-14 | 15-Aug-14 | 12 |
| L16-6221 | Frame Unit Ceilings | 2 | 2 | 15-Aug-14 | 18-Aug-14 | 15 |
| L12-6024 | Inspections for GWB Cover | 1 | 1 | 18-Aug-14 | 18-Aug-14 | 4 |
| L17-6020 | Install Hollow Metal Frames | 3 | 3 | 18-Aug-14 | 20-Aug-14 | 18 |
| L10-6000 | Skim Ceiling/Tape GWB | 6 | 6 | 19-Aug-14 | 26-Aug-14 | 44 |
| L15-6016 | Electrical RI | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 4 |
| L15-6018 | HVAC RI | 3 | 3 | 19-Aug-14 | 21-Aug-14 | 6 |
| L15-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 4 |
| L15-6013 | Fire Sprinkler Branch Lines | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 8 |
| L16-6013 | Fire Sprinkler Branch Lines | 2 | 2 | 19-Aug-14 | 20-Aug-14 | 11 |
| L17-6013 | Fire Sprinkler Branch Lines | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 13 |
| L14-6024 | Inspections for GWB Cover | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 4 |
| L16-6018 | HVAC RI | 3 | 3 | 22-Aug-14 | 26-Aug-14 | 7 |
| L17-6014 | Set Tubs & Plumbing RI | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 6 |
| L11-6000 | Skim Ceiling/Tape GWB | 6 | 6 | 25-Aug-14 | 02-Sep-14 | 40 |
| L16-6016 | Electrical RI | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 4 |
| L16-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 4 |
| L15-6024 | Inspections for GWB Cover | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 4 |
| L12-6000 | Skim Ceiling/Tape GWB | 6 | 6 | 29-Aug-14 | 08-Sep-14 | 36 |
| L17-6018 | HVAC RI | 3 | 3 | 29-Aug-14 | 03-Sep-14 | 6 |
| L17-6221 | Frame Unit Ceilings | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 9 |
| L17-6016 | Electrical RI | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 4 |

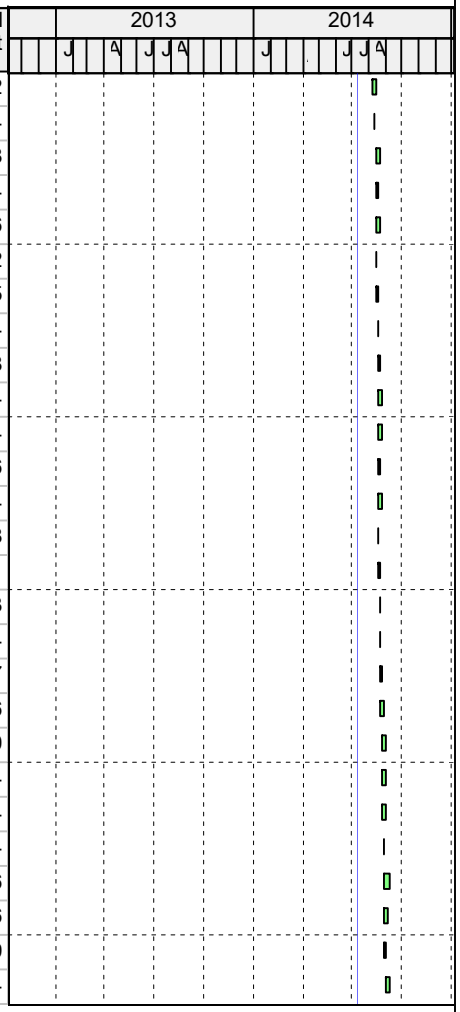



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6022 | Fire Alarm / Elec Specialties Rl | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 4 |
| L16-6024 | Inspections for GWB Cover | 1 | 1 | 04-Sep-14 | 04-Sep-14 | 4 |
| L14-6000 | Skim Ceiling/Tape GWB | 6 | 6 | 05-Sep-14 | 12-Sep-14 | 32 |
| L17-6024 | Inspections for GWB Cover | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 4 |
| L15-6000 | Skim Ceiling/Tape GWB | 6 | 6 | 11-Sep-14 | 18-Sep-14 | 12 |
| L16-6000 | Skim Ceiling/Tape GWB | 6 | 6 | 17-Sep-14 | 24-Sep-14 | 8 |
| L17-6000 | Skim Ceiling/Tape GWB | 4 | 4 | 25-Sep-14 | 30-Sep-14 | 0 |
| **Mechanical Penthouse** | | | | | | |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 0 | 11-Jun-14 A | 20-Jun-14 A | |
| PH-6006 | PH - Exterior Wall Framing (including PH roof parapet | 6 | 1 | 12-Jun-14 A | 14-Jul-14 | 16 |
| PH-6014 | PH - Plumbing/Piping Rl | 40 | 35 | 25-Jun-14 A | 29-Aug-14 | 11 |
| PH-6002 | PH - Layout | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| PH-6008 | PH - Interior Wall Framing | 3 | 3 | 15-Jul-14 | 17-Jul-14 | 17 |
| PH-6020 | PH - H Mtl Frames | 2 | 2 | 16-Jul-14 | 17-Jul-14 | 47 |
| PH-6012 | PH - Fire Sprinkler Rl | 10 | 10 | 18-Jul-14 | 31-Jul-14 | 32 |
| PH-6016 | PH - Electrical Rl | 20 | 20 | 18-Jul-14 | 14-Aug-14 | 22 |
| PH-6018 | PH - HVAC Rl | 25 | 25 | 18-Jul-14 | 21-Aug-14 | 17 |
| PH-6022 | PH - Fire Alarm / Elec Specialties Rl | 4 | 4 | 18-Jul-14 | 23-Jul-14 | 38 |
| PH-6024 | PH - Inspections | 2 | 2 | 02-Sep-14 | 03-Sep-14 | 11 |
| **Finishes** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL4-8100 | LL4 - Insulation | 2 | 2 | 18-Jul-14 | 21-Jul-14 | 37 |
| LL4-8102 | LL4 - GWB Hang / Tape / Finish | 8 | 8 | 22-Jul-14 | 31-Jul-14 | 37 |
| LL4-8104 | LL4 - Int Painting | 3 | 3 | 04-Aug-14 | 06-Aug-14 | 54 |
| LL4-8108 | LL4 - Elec Trim / Finish | 6 | 6 | 07-Aug-14 | 14-Aug-14 | 54 |

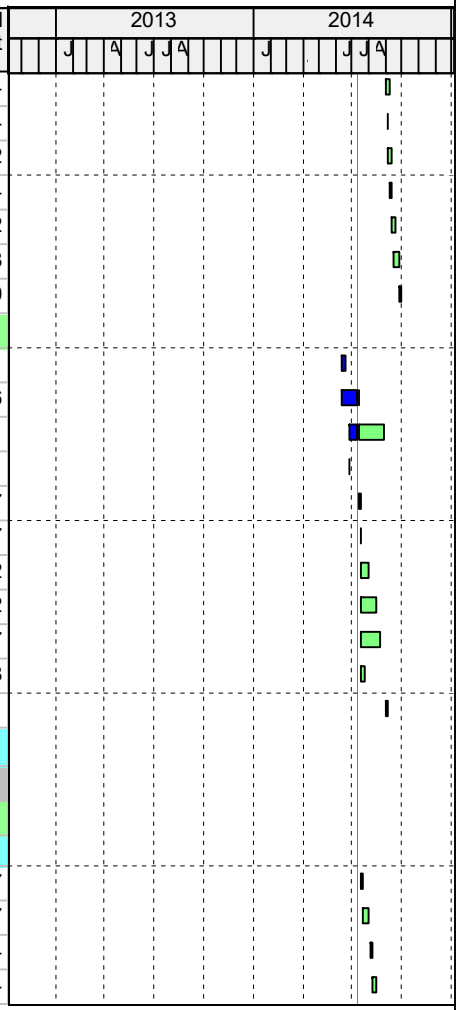


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 59 |
| LL4-8122 | LL4 - Plumbing Trim / Finish | 2 | 2 | 14-Aug-14 | 15-Aug-14 | 61 |
| LL4-8110 | LL4 - HVAC Trim / Finish | 2 | 2 | 15-Aug-14 | 18-Aug-14 | 56 |
| LL4-8118 | LL4 - Elec Specialties Trim / Finish | 4 | 4 | 15-Aug-14 | 20-Aug-14 | 54 |
| LL4-8124 | LL4 - Flooring | 3 | 3 | 21-Aug-14 | 25-Aug-14 | 54 |
| LL4-8126 | LL4 - Doors & Hardware | 3 | 3 | 22-Aug-14 | 26-Aug-14 | 54 |
| LL4-8114 | LL4 - Striping / Signage | 3 | 3 | 26-Aug-14 | 28-Aug-14 | 59 |
| LL4-8130 | LL4 - Substantially Complete | 0 | 0 | | 26-Aug-14 | 54 |
| LL4-8134 | LL4 - Pre-Clean | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 54 |
| LL4-8132 | LL4 - Contractor Pre-Punchlist | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 54 |
| LL4-8208 | LL4 - Final Clean | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 54 |
| LL4-8210 | LL4 - Owner Walk / Create Punchlist | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 54 |
| LL4-8212 | LL4 - Resolve Final Punchlist | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 54 |
| LL4-8214 | LL4 - Floor Complete | 0 | 0 | | 17-Sep-14 | 54 |
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL3-8100 | LL3 - Insulation | 2 | 2 | 22-Jul-14 | 23-Jul-14 | 38 |
| LL3-8102 | LL3 - GWB Hang / Tape / Finish | 8 | 8 | 25-Jul-14 | 05-Aug-14 | 37 |
| LL3-8104 | LL3 - Int Painting | 3 | 3 | 04-Aug-14 | 06-Aug-14 | 59 |
| LL3-8108 | LL3 - Elec Trim / Finish | 6 | 6 | 07-Aug-14 | 14-Aug-14 | 59 |
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 64 |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 2 | 2 | 14-Aug-14 | 15-Aug-14 | 66 |
| LL3-8110 | LL3 - HVAC Trim / Finish | 2 | 2 | 15-Aug-14 | 18-Aug-14 | 61 |
| LL3-8118 | LL3 - Elec Specialties Trim / Finish | 4 | 4 | 15-Aug-14 | 20-Aug-14 | 59 |
| LL3-8124 | LL3 - Flooring | 3 | 3 | 21-Aug-14 | 25-Aug-14 | 59 |
| LL3-8126 | LL3 - Doors & Hardware | 3 | 3 | 22-Aug-14 | 26-Aug-14 | 59 |
| LL3-8114 | LL3 - Striping / Signage | 3 | 3 | 26-Aug-14 | 28-Aug-14 | 64 |

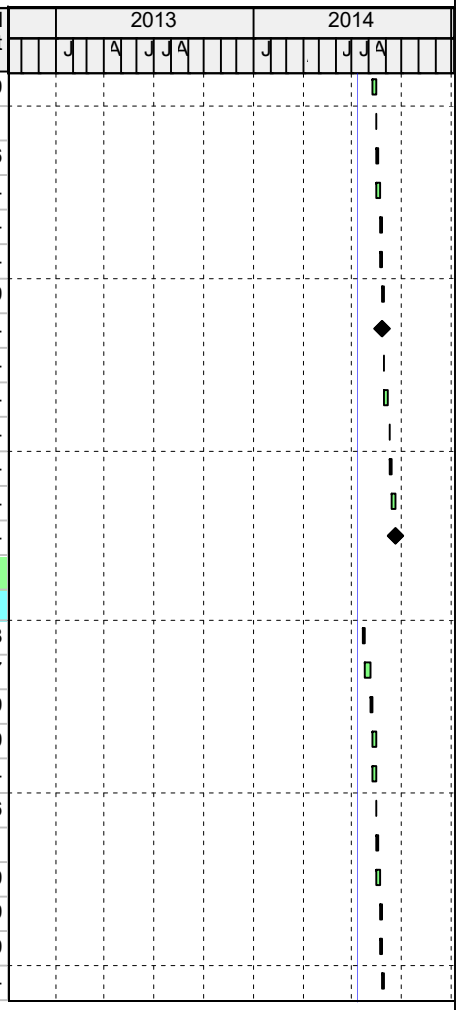



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-8130 | LL3 - Substantially Complete | 0 | 0 | | 26-Aug-14 | 59 |
| LL3-8134 | LL3 - Pre-Clean | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 59 |
| LL3-8132 | LL3 - Contractor Pre-Punchlist | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 59 |
| LL3-8208 | LL3 - Final Clean | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 59 |
| LL3-8210 | LL3 - Owner Walk / Create Punchlist | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 59 |
| LL3-8212 | LL3 - Resolve Final Punchlist | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 54 |
| LL3-8214 | LL3 - Floor Complete | 0 | 0 | | 24-Sep-14 | 54 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 10 | 9 | 02-Jun-14 A | 08-Aug-14 | 71 |
| LL2E-8102 | LL2 - GWB Hang / Tape / Finish @ Electrical Rooms | 8 | 0 | 24-Jun-14 A | 03-Jul-14 A | |
| LL2-8100 | LL2 - Insulation | 3 | 3 | 24-Jul-14 | 28-Jul-14 | 38 |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish | 11 | 11 | 04-Aug-14 | 18-Aug-14 | 34 |
| LL2-8104 | LL2 - Int Painting | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 34 |
| LL2-8120 | LL2 - Steel Pipe Guardrails | 6 | 6 | 19-Aug-14 | 26-Aug-14 | 64 |
| LL2-8108 | LL2 - Elec Trim / Finish | 10 | 10 | 21-Aug-14 | 04-Sep-14 | 34 |
| LL2-8112 | LL2 - Fire Sprinkler Trim / Finish | 8 | 8 | 21-Aug-14 | 02-Sep-14 | 48 |
| LL2-8116 | LL2 - Finish Carpentry / Millwork | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 54 |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 9 | 9 | 21-Aug-14 | 03-Sep-14 | 54 |
| LL2-8122 | LL2 - Plumbing Trim / Finish | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 55 |
| LL2-8128 | LL2 - Entry Gates | 3 | 3 | 04-Sep-14 | 08-Sep-14 | 54 |
| LL2-8110 | LL2 - HVAC Trim / Finish | 12 | 12 | 05-Sep-14 | 22-Sep-14 | 34 |
| LL2-8118 | LL2 - Elec Specialties Trim / Finish | 4 | 4 | 05-Sep-14 | 10-Sep-14 | 42 |
| LL2-8136 | LL2 - Chainlink Fencing / Gate @ Recycling | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 54 |
| LL2-8124 | LL2 - Flooring | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 34 |
| LL2-8114 | LL2 - Striping / Signage | 3 | 3 | 30-Sep-14 | 02-Oct-14 | 45 |
| LL2-8126 | LL2 - Doors & Hardware | 7 | 7 | 30-Sep-14 | 08-Oct-14 | 34 |

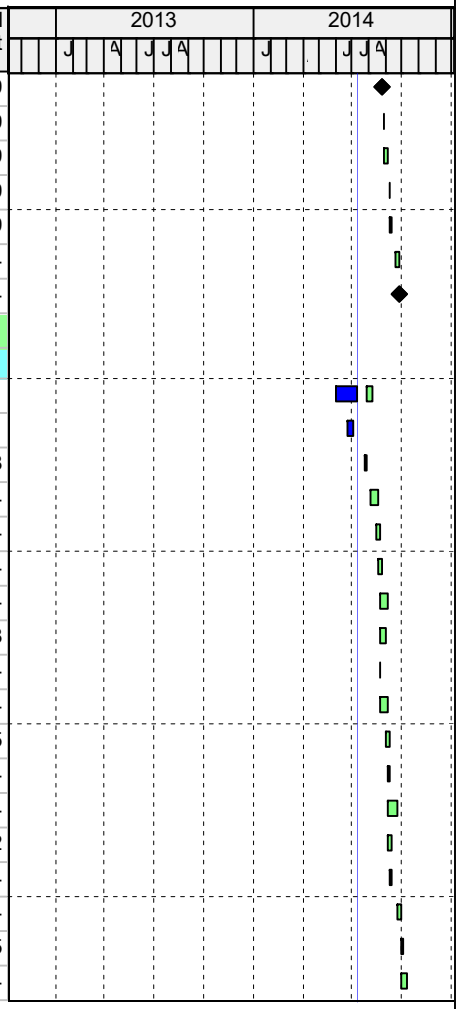



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-8130 | LL2 - Substantially Complete | 0 | 0 | | 08-Oct-14 | 34 |
| LL2-8134 | LL2 - Pre-Clean | 2 | 2 | 09-Oct-14 | 10-Oct-14 | 34 |
| LL2-8132 | LL2 - Contractor Pre-Punchlist | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 34 |
| LL2-8208 | LL2 - Final Clean | 2 | 2 | 20-Oct-14 | 21-Oct-14 | 34 |
| LL2-8210 | LL2 - Owner Walk / Create Punchlist | 1 | 1 | 22-Oct-14 | 22-Oct-14 | 34 |
| LL2-8212 | LL2 - Resolve Final Punchlist | 5 | 5 | 23-Oct-14 | 29-Oct-14 | 34 |
| LL2-8214 | LL2 - Floor Complete | 0 | 0 | | 29-Oct-14 | 34 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1U-8102 | Above Ceiling GWB | 5 | 1 | 10-Feb-14 A | 14-Jul-14 | 23 |
| LL1-Z2U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 09-May-14 A | |
| LL1-Z3U-8102 | Above Ceiling GWB (At All Areas North of Q-Line) | 5 | 0 | 10-Feb-14 A | 20-Jun-14 A | |
| L1BU-8102 | Above Ceiling GWB [including East Service Corridor] | 5 | 0 | 06-Jun-14 A | 11-Jun-14 A | |
| L1LU-8102 | Above Ceiling GWB [including back of house] | 5 | 4 | 24-Jun-14 A | 23-Jul-14 | 4 |
| L1KU-8102 | Above Ceiling GWB [including public restroom] | 2 | 1 | 26-Jun-14 A | 16-Jul-14 | 8 |
| LL1-8100 | Insulation | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 21 |
| LL1-Z2-8100 | Insulation | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 15 |
| LL1-8102 | GWB Hang | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 21 |
| L1B-8100 | Insulation | 4 | 4 | 13-Aug-14 | 18-Aug-14 | 21 |
| LL1-Z2-8102 | GWB Hang | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 15 |
| LL1-8215 | GWB Tape | 7 | 7 | 18-Aug-14 | 26-Aug-14 | 21 |
| L1B-8102 | GWB Hang | 6 | 6 | 19-Aug-14 | 26-Aug-14 | 21 |
| LL1-Z2-8215 | GWB Tape | 7 | 7 | 21-Aug-14 | 29-Aug-14 | 15 |
| LL1-Z3-8100 | Insulation | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 17 |
| LL1-Z3-8102 | GWB Hang | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 17 |
| LL1-8104 | Prime Paint | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 21 |
| L1B-8215 | GWB Tape | 7 | 7 | 27-Aug-14 | 05-Sep-14 | 21 |

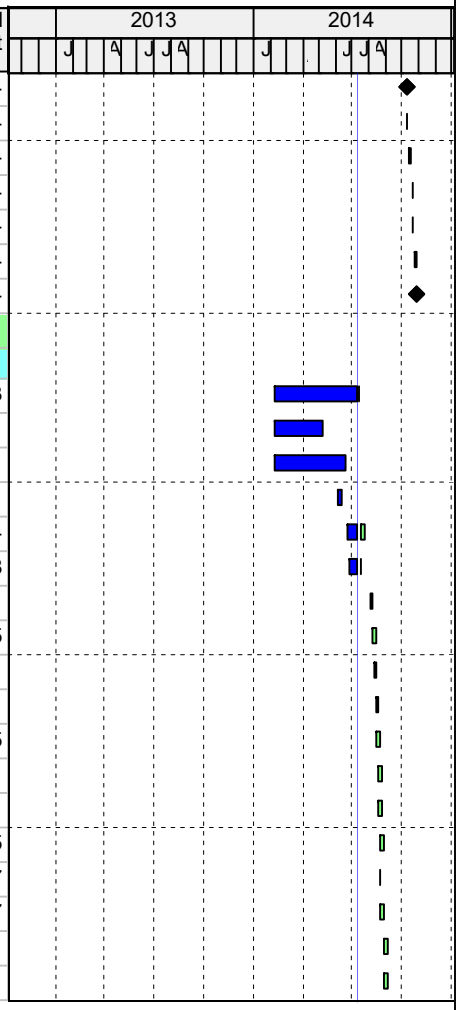


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8215 | GWB Tape | 7 | 7 | 29-Aug-14 | 09-Sep-14 | 17 |
| LL1-Z2-8104 | Prime Paint | 5 | 5 | 02-Sep-14 | 08-Sep-14 | 15 |
| LL1-8116 | Finish Carpentry / Millwork | 10 | 10 | 04-Sep-14 | 17-Sep-14 | 21 |
| LL1-8114 | T Bar Grid Ceiling | 3 | 3 | 04-Sep-14 | 08-Sep-14 | 33 |
| L1L-8100 | Insulation | 5 | 5 | 05-Sep-14 | 11-Sep-14 | 4 |
| L1B-8104 | Prime Paint | 3 | 3 | 08-Sep-14 | 10-Sep-14 | 21 |
| L1K-8100 | Insulation | 3 | 3 | 08-Sep-14 | 10-Sep-14 | 8 |
| LL1-Z2-8114 | T Bar Grid Ceiling | 6 | 6 | 09-Sep-14 | 16-Sep-14 | 29 |
| LL1-Z3-8104 | Prime Paint | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 17 |
| L1B-8116 | Finish Carpentry / Millwork | 10 | 10 | 11-Sep-14 | 24-Sep-14 | 21 |
| L1K-8102 | GWB Hang | 4 | 4 | 11-Sep-14 | 16-Sep-14 | 8 |
| LL1-Z3-8114 | T Bar Grid Ceiling | 2 | 2 | 12-Sep-14 | 15-Sep-14 | 17 |
| L1L-8102 | GWB Hang | 7 | 7 | 12-Sep-14 | 22-Sep-14 | 4 |
| LL1-Z2-8116 | Finish Carpentry / Millwork | 10 | 10 | 16-Sep-14 | 29-Sep-14 | 15 |
| LL1-Z3-8116 | Finish Carpentry / Millwork | 3 | 3 | 16-Sep-14 | 18-Sep-14 | 17 |
| L1K-8215 | GWB Tape | 6 | 6 | 17-Sep-14 | 24-Sep-14 | 8 |
| L1B-8114 | T Bar Grid Ceiling | 3 | 3 | 22-Sep-14 | 24-Sep-14 | 21 |
| LL1-Z3-8124 | Flooring | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 17 |
| L1L-8215 | GWB Tape | 9 | 9 | 23-Sep-14 | 03-Oct-14 | 4 |
| LL1-8124 | Flooring | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 21 |
| LL1-Z3-8126 | Doors & Hardware | 1 | 1 | 25-Sep-14 | 25-Sep-14 | 36 |
| LL1-Z3-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 3 | 3 | 25-Sep-14 | 29-Sep-14 | 41 |
| L1K-8104 | Prime Paint | 3 | 3 | 25-Sep-14 | 29-Sep-14 | 8 |
| LL1-Z3-8106 | Wallcoverings | 2 | 2 | 26-Sep-14 | 29-Sep-14 | 36 |
| LL1-Z3-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 41 |
| LL1-Z3-8118 | Elec & Specialties Trim / Finish | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 39 |
| L1K-8116 | Finish Carpentry / Millwork | 7 | 7 | 30-Sep-14 | 08-Oct-14 | 8 |

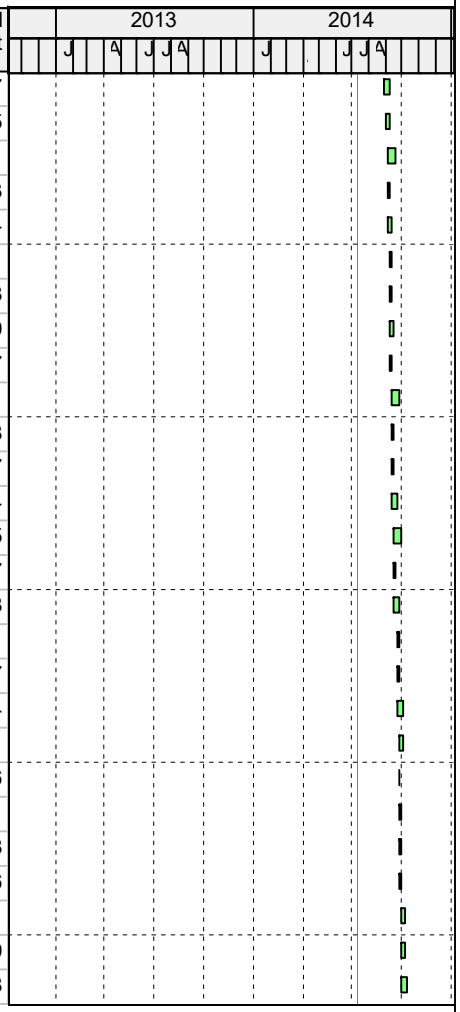



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8114 | T Bar Grid Ceiling | 3 | 3 | 30-Sep-14 | 02-Oct-14 | 15 |
| LL1-8126 | Doors & Hardware | 3 | 3 | 02-Oct-14 | 06-Oct-14 | 21 |
| LL1-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 2 | 2 | 02-Oct-14 | 03-Oct-14 | 37 |
| L1B-8124 | Flooring | 5 | 5 | 02-Oct-14 | 08-Oct-14 | 21 |
| L1L-8104 | Prime Paint | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 4 |
| LL1-8106 | Wallcoverings | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 21 |
| LL1-Z2-8124 | Flooring | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 15 |
| LL1-Z3-8134 | Pre-Clean | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 39 |
| L1B-8126 | Doors & Hardware | 2 | 2 | 09-Oct-14 | 10-Oct-14 | 21 |
| L1B-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 2 | 2 | 09-Oct-14 | 10-Oct-14 | 29 |
| L1L-8116 | Finish Carpentry / Millwork | 10 | 10 | 09-Oct-14 | 22-Oct-14 | 4 |
| L1L-8114 | Install wood ceiling supports | 3 | 3 | 09-Oct-14 | 13-Oct-14 | 4 |
| LL1-Z3-8132 | Contractor Pre-Punchlist | 3 | 3 | 10-Oct-14 | 14-Oct-14 | 39 |
| L1B-8106 | Wallcoverings | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 21 |
| LL1-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 31 |
| LL1-8118 | Elec & Specialties Trim / Finish | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 21 |
| LL1-Z2-8126 | Doors & Hardware | 3 | 3 | 14-Oct-14 | 16-Oct-14 | 15 |
| LL1-Z2-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 26 |
| L1L-8124 | Flooring | 15 | 15 | 14-Oct-14 | 03-Nov-14 | 4 |
| L1K-8124 | Flooring | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 8 |
| LL1-Z2-8106 | Wallcoverings | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 15 |
| L1B-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 24 |
| L1B-8118 | Elec & Specialties Trim / Finish | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 21 |
| L1K-8126 | Doors & Hardware | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 8 |
| L1K-8140 | Acoustical Ceiling Tile (for sprinkler trim, FA trim, perim | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 23 |
| LL1-Z2-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 24-Oct-14 | 30-Oct-14 | 23 |
| LL1-Z2-8118 | Elec & Specialties Trim / Finish | 5 | 5 | 24-Oct-14 | 30-Oct-14 | 15 |

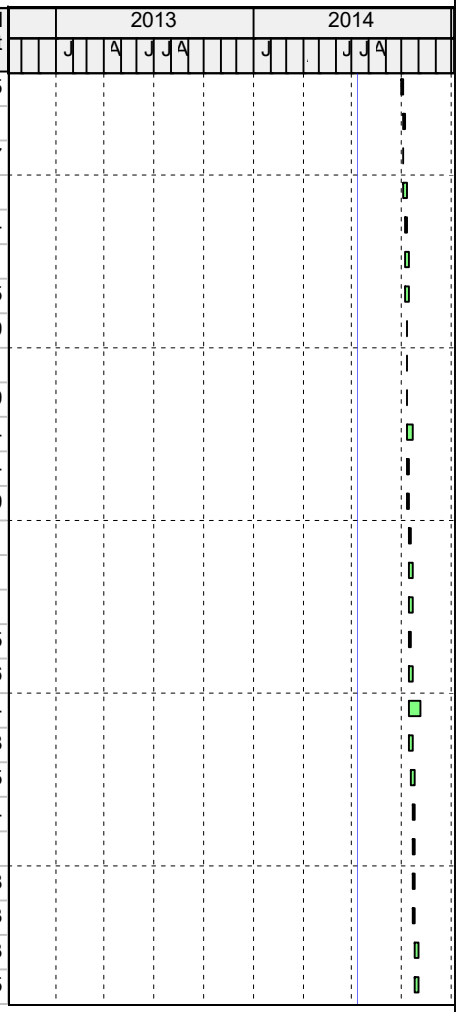



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8106 | Wallcoverings | 5 | 5 | 24-Oct-14 | 30-Oct-14 | 8 |
| LL1-8134 | Pre-Clean | 2 | 2 | 28-Oct-14 | 29-Oct-14 | 21 |
| LL1-8132 | Contractor Pre-Punchlist | 5 | 5 | 30-Oct-14 | 05-Nov-14 | 21 |
| L1B-8134 | Pre-Clean | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 21 |
| L1K-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 31-Oct-14 | 06-Nov-14 | 18 |
| L1K-8118 | Elec & Specialties Trim / Finish | 10 | 10 | 31-Oct-14 | 14-Nov-14 | 8 |
| L1B-8132 | Contractor Pre-Punchlist | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 21 |
| LL1-Z2-8134 | Pre-Clean | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 15 |
| L1L-8126 | Doors & Hardware | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 4 |
| L1L-8140 | Install wood ceiling | 8 | 8 | 05-Nov-14 | 17-Nov-14 | 7 |
| LL1-Z2-8132 | Contractor Pre-Punchlist | 5 | 5 | 07-Nov-14 | 14-Nov-14 | 15 |
| L1L-8106 | Wallcoverings | 5 | 5 | 11-Nov-14 | 17-Nov-14 | 4 |
| L1L-8118 | Elec & Specialties Trim / Finish | 7 | 7 | 14-Nov-14 | 24-Nov-14 | 4 |
| L1L-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 7 |
| L1K-8134 | Pre-Clean | 2 | 2 | 20-Nov-14 | 21-Nov-14 | 8 |
| L1K-8132 | Contractor Pre-Punchlist | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 8 |
| L1L-8134 | Pre-Clean | 2 | 2 | 25-Nov-14 | 26-Nov-14 | 4 |
| L1L-8132 | Contractor Pre-Punchlist | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 4 |
| **Corridors / Common / Public Areas** | | | | | | |
| LL1-8200 | First Coat Finish Paint | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 21 |
| LL1-Z3-8200 | First Coat Finish Paint | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 17 |
| L1B-8200 | First Coat Finish Paint | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 21 |
| LL1-Z3-8201 | Final Coat Finish Paint | 2 | 2 | 26-Sep-14 | 29-Sep-14 | 36 |
| LL1-Z2-8200 | First Coat Finish Paint | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 15 |
| LL1-Z3-8204 | Mech Trim / Finish (HVAC & Plumbing) | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 36 |
| LL1-8201 | Final Coat Finish Paint | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 21 |
| L1K-8200 | First Coat Finish Paint | 3 | 3 | 09-Oct-14 | 13-Oct-14 | 8 |

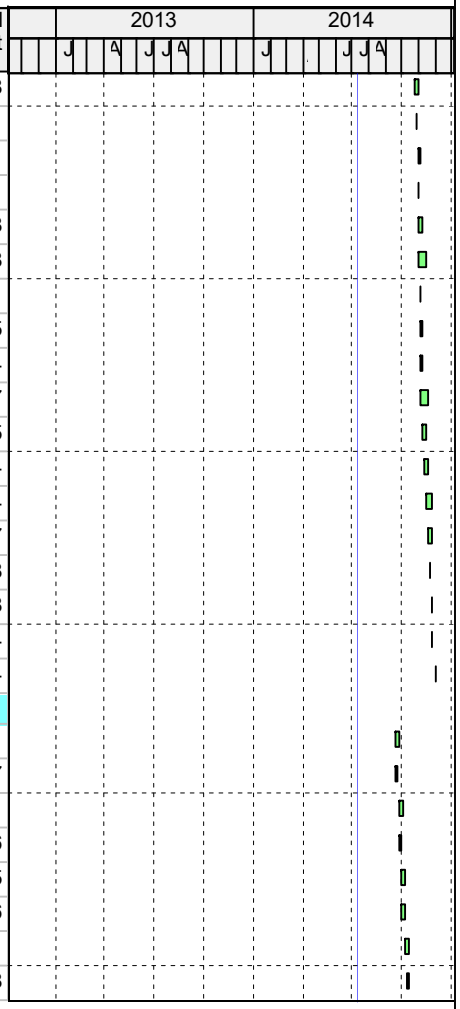



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-8201 | Final Coat Finish Paint | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 21 |
| LL1-8204 | Mech Trim / Finish (HVAC & Plumbing) | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 21 |
| LL1-Z3-8208 | Final Clean | 2 | 2 | 15-Oct-14 | 16-Oct-14 | 39 |
| LL1-Z2-8201 | Final Coat Finish Paint | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 15 |
| LL1-Z3-8210 | Owner Walk / Create Punchlist | 1 | 1 | 17-Oct-14 | 17-Oct-14 | 39 |
| LL1-Z3-8212 | Resolve Final Punchlist | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 39 |
| L1B-8204 | Mech Trim / Finish (HVAC & Plumbing) | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 21 |
| LL1-Z3-8214 | LL1 Food Prep Complete | 0 | 0 | | 22-Oct-14 | 39 |
| L1L-8200 | First Coat Finish Paint | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 4 |
| LL1-Z2-8204 | Mech Trim / Finish (HVAC & Plumbing) | 5 | 5 | 24-Oct-14 | 30-Oct-14 | 15 |
| L1K-8201 | Final Coat Finish Paint | 5 | 5 | 24-Oct-14 | 30-Oct-14 | 8 |
| L1K-8204 | Mech Trim / Finish (HVAC & Plumbing) | 10 | 10 | 31-Oct-14 | 14-Nov-14 | 8 |
| LL1-8208 | Final Clean | 2 | 2 | 06-Nov-14 | 07-Nov-14 | 21 |
| L1B-8208 | Final Clean | 2 | 2 | 06-Nov-14 | 07-Nov-14 | 21 |
| LL1-8210 | Owner Walk / Create Punchlist | 1 | 1 | 11-Nov-14 | 11-Nov-14 | 21 |
| L1B-8210 | Owner Walk / Create Punchlist | 1 | 1 | 11-Nov-14 | 11-Nov-14 | 21 |
| L1L-8201 | Final Coat Finish Paint | 3 | 3 | 11-Nov-14 | 13-Nov-14 | 4 |
| LL1-8212 | Resolve Final Punchlist | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 21 |
| L1B-8212 | Resolve Final Punchlist | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 21 |
| LL1-Z2-8208 | Final Clean | 2 | 2 | 17-Nov-14 | 18-Nov-14 | 15 |
| L1L-8204 | Mech Trim / Finish (HVAC & Plumbing) | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 4 |
| LL1-8214 | LL1 Meeting /Board Rooms Complete | 0 | 0 | | 18-Nov-14 | 21 |
| L1B-8214 | L1 Ballrooms Complete | 0 | 0 | | 18-Nov-14 | 21 |
| LL1-Z2-8210 | Owner Walk / Create Punchlist | 1 | 1 | 19-Nov-14 | 19-Nov-14 | 15 |
| LL1-Z2-8212 | Resolve Final Punchlist | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 15 |
| LL1-Z2-8214 | LL1 Junior Ballrooms Complete | 0 | 0 | | 26-Nov-14 | 15 |
| L1K-8208 | Final Clean | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 8 |

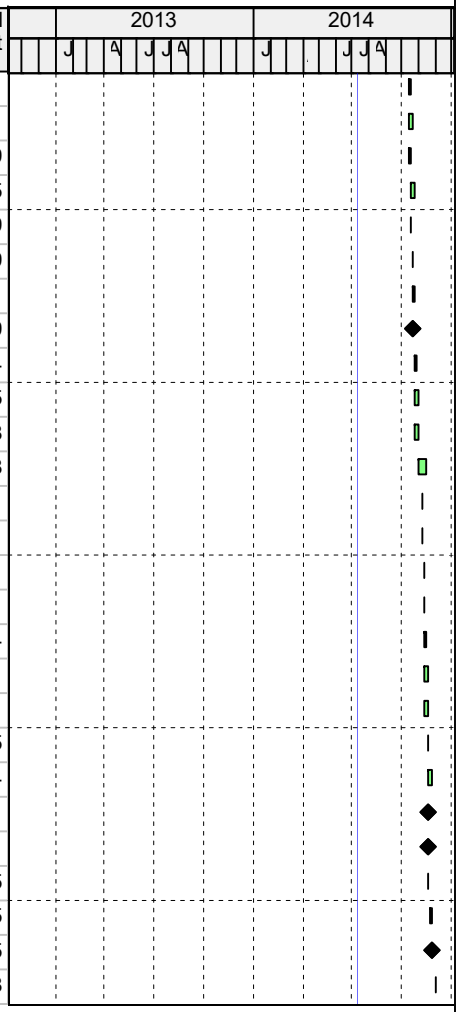



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8210 | Owner Walk / Create Punchlist | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 8 |
| L1L-8208 | Final Clean | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 4 |
| L1K-8212 | Resolve Final Punchlist | 4 | 4 | 04-Dec-14 | 09-Dec-14 | 8 |
| L1L-8210 | Owner Walk / Create Punchlist | 1 | 1 | 08-Dec-14 | 08-Dec-14 | 4 |
| L1L-8212 | Resolve Final Punchlist | 5 | 5 | 09-Dec-14 | 15-Dec-14 | 4 |
| L1K-8214 | L1 Kitchen Complete | 0 | 0 | | 09-Dec-14 | 8 |
| L1L-8214 | L1 Common Areas Complete | 0 | 0 | | 15-Dec-14 | 4 |
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8100 | L2 - Insulation | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 21 |
| L02-8102 | L2 - GWB Hang / Tape / Finish - (Including Common / | 15 | 15 | 22-Aug-14 | 12-Sep-14 | 21 |
| L02-8104 | L2 - Int Painting | 10 | 10 | 10-Sep-14 | 23-Sep-14 | 21 |
| L02-8106 | L2 - Wallcoverings | 6 | 6 | 12-Sep-14 | 19-Sep-14 | 33 |
| L02-8116 | L2 - Finish Carpentry / Millwork | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 26 |
| L02-8120 | L2 - Ceramic Tile / Counter Tops | 8 | 8 | 19-Sep-14 | 30-Sep-14 | 26 |
| L02-8122 | L2 - Plumbing Trim / Finish | 8 | 8 | 23-Sep-14 | 02-Oct-14 | 28 |
| L02-8108 | L2 - Elec Trim / Finish | 10 | 10 | 24-Sep-14 | 07-Oct-14 | 21 |
| L02-8110 | L2 - HVAC Trim / Finish | 10 | 10 | 24-Sep-14 | 07-Oct-14 | 21 |
| L02-8112 | L2 - Fire Sprinkler Trim / Finish | 8 | 8 | 24-Sep-14 | 03-Oct-14 | 23 |
| L02-8118 | L2 - Elec Specialties Trim / Finish | 10 | 10 | 24-Sep-14 | 07-Oct-14 | 21 |
| L02-8136 | L2 - Lockers / Benches @ Locker Rooms | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 32 |
| L02-8128 | L2 - Bath Specialties | 2 | 2 | 03-Oct-14 | 06-Oct-14 | 28 |
| L02-8124 | L2 - Flooring | 5 | 5 | 08-Oct-14 | 14-Oct-14 | 21 |
| L02-8126 | L2 - Doors & Hardware | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 21 |
| L02-8130 | L2 - Admin / Employee Rooms Substantially Complet | 0 | 0 | | 15-Oct-14 | 21 |
| L02-8134 | L2 - Pre-Clean | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 24 |
| L02-8132 | L2 - Contractor Pre-Punchlist | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 24 |

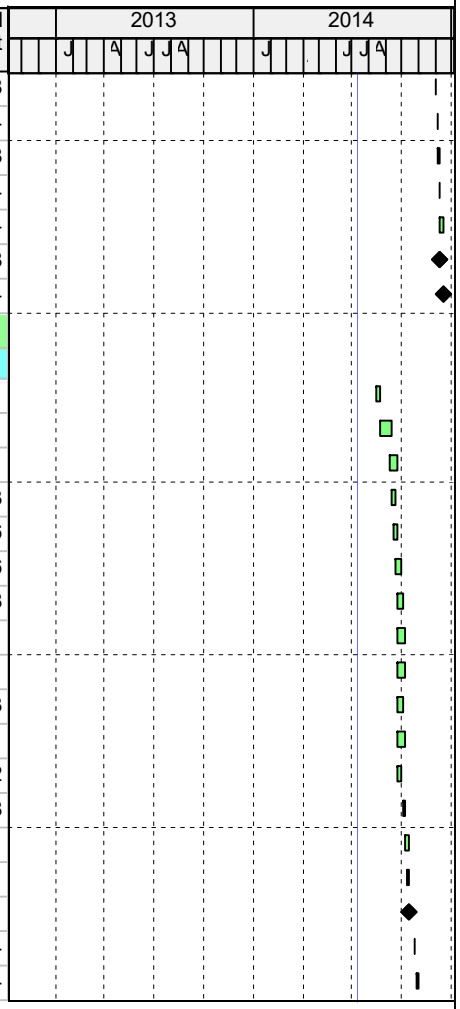



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Corridors** | | | | | | |
| L02-8200 | L2 - Final Paint @ Common / Public Areas | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 21 |
| L02-8114 | L2 - Signage | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 28 |
| L02-8202 | L2 - Elec Trim / Finish @ Common / Public Areas | 5 | 5 | 23-Oct-14 | 29-Oct-14 | 22 |
| L02-8204 | L2 - Mech Trim / Finish @ Common / Public Areas (H | 5 | 5 | 23-Oct-14 | 29-Oct-14 | 21 |
| L02-8206 | L2 - Flooring @ Corridors | 5 | 5 | 30-Oct-14 | 05-Nov-14 | 21 |
| L02-8208 | L2 - Final Clean | 2 | 2 | 06-Nov-14 | 07-Nov-14 | 21 |
| L02-8210 | L2 - Owner Walk / Create Punchlist | 1 | 1 | 11-Nov-14 | 11-Nov-14 | 21 |
| L02-8212 | L2 - Resolve Final Punchlist | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 21 |
| L02-8214 | L2 - Floor Complete | 0 | 0 | | 18-Nov-14 | 21 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L03-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L04-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L05-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L06-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L07-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L08-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L09-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L10-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L11-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L12-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L14-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L15-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L16-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L17-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |

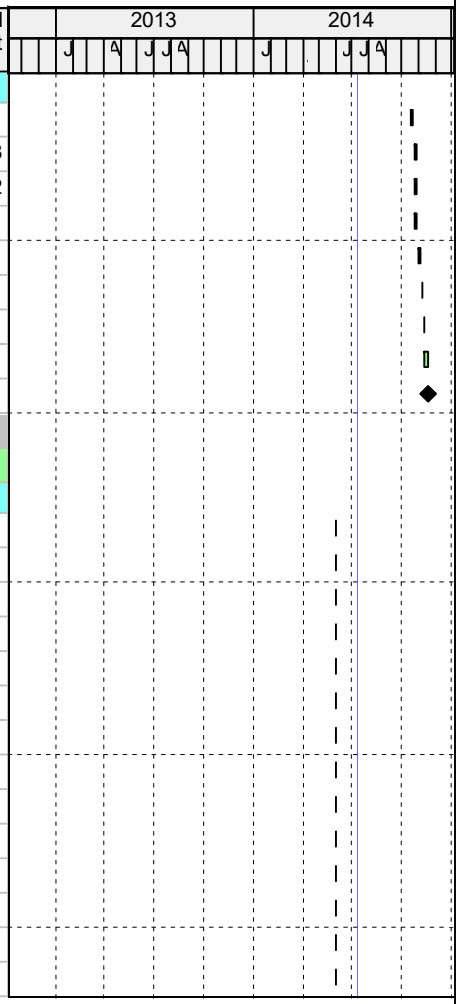



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8102S | Stock GWB | 2 | 0 | 27-Jun-14 A | 08-Jul-14 A | |
| L04-8102 | Hang GWB/Install Sound Batts | 4 | 1 | 07-Jul-14 A | 15-Jul-14 | 0 |
| L04-8102S | Stock GWB | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-8102 | Hang GWB/Install Sound Batts | 5 | 1 | 09-Jul-14 A | 14-Jul-14 | 0 |
| L05-8102S | Stock GWB | 2 | 1 | 10-Jul-14 A | 14-Jul-14 | 1 |
| L06-8102S | Stock GWB | 2 | 2 | 14-Jul-14 | 15-Jul-14 | 4 |
| L05-8102 | Hang GWB/Install Sound Batts | 4 | 4 | 16-Jul-14 | 21-Jul-14 | 0 |
| L03-8104 | Primer Paint Coat | 2 | 2 | 17-Jul-14 | 18-Jul-14 | 57 |
| L07-8102S | Stock GWB | 2 | 2 | 18-Jul-14 | 21-Jul-14 | 4 |
| L03-8128 | Install Tub Surrounds | 5 | 5 | 21-Jul-14 | 25-Jul-14 | 57 |
| L04-8104 | Primer Paint Coat | 2 | 2 | 22-Jul-14 | 23-Jul-14 | 54 |
| L06-8102 | Hang GWB/Install Sound Batts | 4 | 4 | 22-Jul-14 | 25-Jul-14 | 0 |
| L03-8120 | Install Bathroom Countertops | 5 | 5 | 23-Jul-14 | 29-Jul-14 | 57 |
| L03-8105 | First Coat Finish Paint | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 57 |
| L04-8128 | Install Tub Surrounds | 5 | 5 | 24-Jul-14 | 30-Jul-14 | 54 |
| L08-8102S | Stock GWB | 2 | 2 | 24-Jul-14 | 25-Jul-14 | 4 |
| L03-8124 | Flooring | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 57 |
| L04-8120 | Install Bathroom Countertops | 5 | 5 | 28-Jul-14 | 01-Aug-14 | 54 |
| L07-8102 | Hang GWB/Install Sound Batts | 4 | 4 | 28-Jul-14 | 31-Jul-14 | 0 |
| L03-8116 | Install Wood Base | 5 | 5 | 29-Jul-14 | 04-Aug-14 | 57 |
| L04-8105 | First Coat Finish Paint | 5 | 5 | 29-Jul-14 | 04-Aug-14 | 54 |
| L05-8104 | Primer Paint Coat | 2 | 2 | 30-Jul-14 | 31-Jul-14 | 48 |
| L09-8102S | Stock GWB | 2 | 2 | 30-Jul-14 | 31-Jul-14 | 4 |
| L03-8107 | Final Coat Finish Paint | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 57 |
| L04-8124 | Flooring | 5 | 5 | 31-Jul-14 | 06-Aug-14 | 54 |
| L03-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 01-Aug-14 | 07-Aug-14 | 57 |
| L04-8116 | Install Wood Base | 5 | 5 | 01-Aug-14 | 07-Aug-14 | 54 |

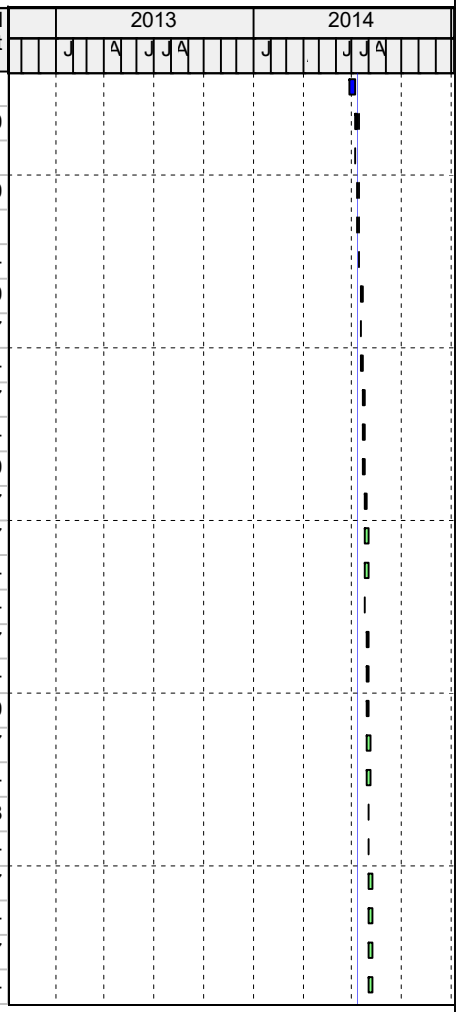



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8128 | Install Tub Surrounds | 5 | 5 | 01-Aug-14 | 07-Aug-14 | 48 |
| L08-8102 | Hang GWB/Install Sound Batts | 4 | 4 | 01-Aug-14 | 06-Aug-14 | 0 |
| L03-8108 | Elec Trim / Finish | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 57 |
| L03-8118 | Elec Specialties Trim / Finish | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 57 |
| L04-8107 | Final Coat Finish Paint | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 54 |
| L05-8120 | Install Bathroom Countertops | 5 | 5 | 05-Aug-14 | 11-Aug-14 | 48 |
| L06-8104 | Primer Paint Coat | 2 | 2 | 05-Aug-14 | 06-Aug-14 | 60 |
| L10-8102S | Stock GWB | 2 | 2 | 05-Aug-14 | 06-Aug-14 | 4 |
| L03-8110 | HVAC Trim / Finish | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 57 |
| L04-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 54 |
| L05-8105 | First Coat Finish Paint | 5 | 5 | 06-Aug-14 | 12-Aug-14 | 48 |
| L03-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 57 |
| L04-8108 | Elec Trim / Finish | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 54 |
| L06-8128 | Install Tub Surrounds | 5 | 5 | 07-Aug-14 | 13-Aug-14 | 60 |
| L09-8102 | Hang GWB/Install Sound Batts | 4 | 4 | 07-Aug-14 | 12-Aug-14 | 0 |
| L03-8126 | Doors & Hardware | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 73 |
| L04-8118 | Elec Specialties Trim / Finish | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 54 |
| L05-8124 | Flooring | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 48 |
| L03-8114 | Signage (By Owner) | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 73 |
| L04-8110 | HVAC Trim / Finish | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 54 |
| L05-8116 | Install Wood Base | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 48 |
| L06-8120 | Install Bathroom Countertops | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 60 |
| L07-8104 | Primer Paint Coat | 2 | 2 | 11-Aug-14 | 12-Aug-14 | 56 |
| L11-8102S | Stock GWB | 2 | 2 | 11-Aug-14 | 12-Aug-14 | 4 |
| L03-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 12-Aug-14 | 14-Aug-14 | 74 |
| L04-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 54 |
| L06-8105 | First Coat Finish Paint | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 60 |

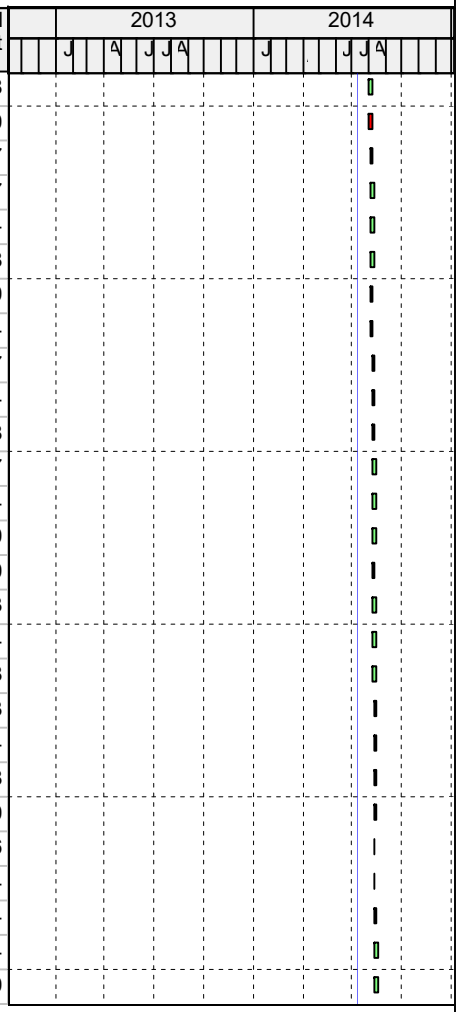



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8126 | Doors & Hardware | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 70 |
| L05-8107 | Final Coat Finish Paint | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 48 |
| L07-8128 | Install Tub Surrounds | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 56 |
| L10-8102 | Hang GWB/Install Sound Batts | 4 | 4 | 13-Aug-14 | 18-Aug-14 | 0 |
| L04-8114 | Signage (By Owner) | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 70 |
| L05-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 48 |
| L06-8124 | Flooring | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 60 |
| L04-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 15-Aug-14 | 19-Aug-14 | 71 |
| L05-8108 | Elec Trim / Finish | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 48 |
| L06-8116 | Install Wood Base | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 60 |
| L07-8120 | Install Bathroom Countertops | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 56 |
| L08-8104 | Primer Paint Coat | 2 | 2 | 15-Aug-14 | 18-Aug-14 | 52 |
| L12-8102S | Stock GWB | 2 | 2 | 15-Aug-14 | 18-Aug-14 | 4 |
| L05-8118 | Elec Specialties Trim / Finish | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 48 |
| L07-8105 | First Coat Finish Paint | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 56 |
| L05-8110 | HVAC Trim / Finish | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 48 |
| L06-8107 | Final Coat Finish Paint | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 60 |
| L08-8128 | Install Tub Surrounds | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 52 |
| L11-8102 | Hang GWB/Install Sound Batts | 4 | 4 | 19-Aug-14 | 22-Aug-14 | 0 |
| L05-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 48 |
| L06-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 60 |
| L07-8124 | Flooring | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 56 |
| L05-8126 | Doors & Hardware | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 64 |
| L06-8108 | Elec Trim / Finish | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 60 |
| L07-8116 | Install Wood Base | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 56 |
| L08-8120 | Install Bathroom Countertops | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 52 |
| L09-8104 | Primer Paint Coat | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 48 |

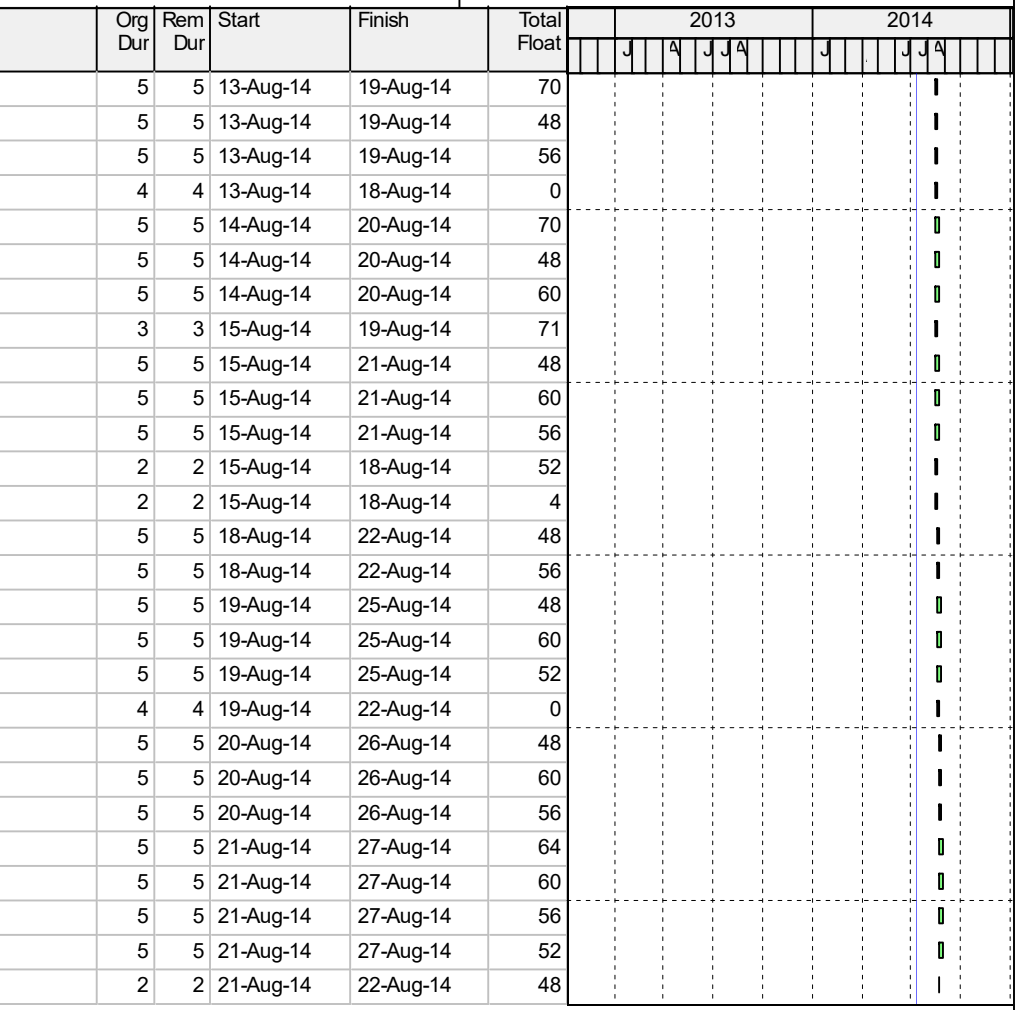



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8102S | Stock GWB | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 4 |
| L05-8114 | Signage (By Owner) | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 64 |
| L06-8118 | Elec Specialties Trim / Finish | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 60 |
| L08-8105 | First Coat Finish Paint | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 52 |
| L05-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 25-Aug-14 | 27-Aug-14 | 65 |
| L06-8110 | HVAC Trim / Finish | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 60 |
| L07-8107 | Final Coat Finish Paint | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 56 |
| L09-8128 | Install Tub Surrounds | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 48 |
| L12-8102 | Hang GWB/Install Sound Batts | 4 | 4 | 25-Aug-14 | 28-Aug-14 | 0 |
| L06-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 60 |
| L07-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 56 |
| L08-8124 | Flooring | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 52 |
| L06-8126 | Doors & Hardware | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 60 |
| L07-8108 | Elec Trim / Finish | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 56 |
| L08-8116 | Install Wood Base | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 52 |
| L09-8120 | Install Bathroom Countertops | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 48 |
| L10-8104 | Primer Paint Coat | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 44 |
| L15-8102S | Stock GWB | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 4 |
| L06-8114 | Signage (By Owner) | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 60 |
| L07-8118 | Elec Specialties Trim / Finish | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 56 |
| L09-8105 | First Coat Finish Paint | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 48 |
| L03-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 28-Aug-14 | 64 |
| L04-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 28-Aug-14 | 64 |
| L03-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 64 |
| L03-8134 | Pre-Clean Guestrooms | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 67 |
| L04-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 64 |
| L04-8134 | Pre-Clean Guestrooms | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 67 |

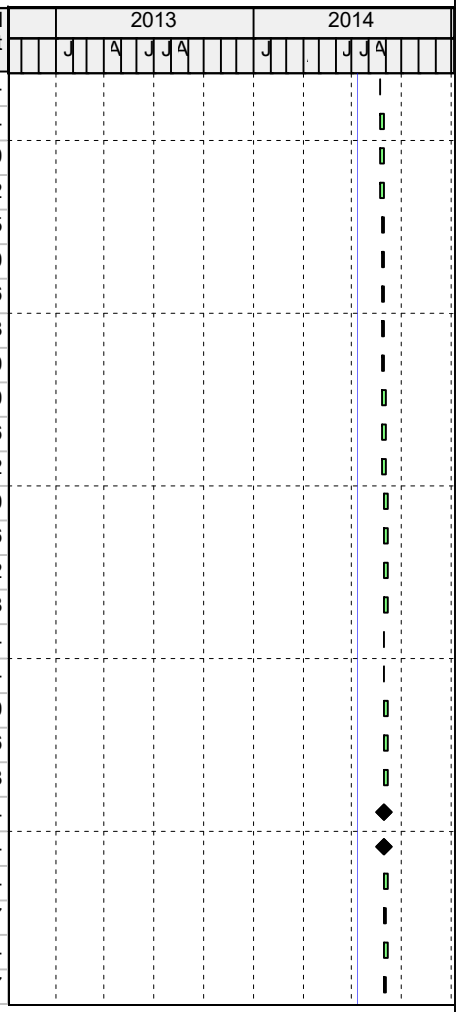



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 29-Aug-14 | 03-Sep-14 | 61 |
| L07-8110 | HVAC Trim / Finish | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 56 |
| L08-8107 | Final Coat Finish Paint | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 52 |
| L10-8128 | Install Tub Surrounds | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 44 |
| L14-8102 | Hang GWB/Install Sound Batts | 4 | 4 | 29-Aug-14 | 04-Sep-14 | 0 |
| L07-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 02-Sep-14 | 08-Sep-14 | 56 |
| L08-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 02-Sep-14 | 08-Sep-14 | 52 |
| L09-8124 | Flooring | 5 | 5 | 02-Sep-14 | 08-Sep-14 | 48 |
| L07-8126 | Doors & Hardware | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 56 |
| L08-8108 | Elec Trim / Finish | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 52 |
| L09-8116 | Install Wood Base | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 48 |
| L10-8120 | Install Bathroom Countertops | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 44 |
| L11-8104 | Primer Paint Coat | 2 | 2 | 03-Sep-14 | 04-Sep-14 | 40 |
| L16-8102S | Stock GWB | 2 | 2 | 03-Sep-14 | 04-Sep-14 | 4 |
| L07-8114 | Signage (By Owner) | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 56 |
| L08-8118 | Elec Specialties Trim / Finish | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 52 |
| L10-8105 | First Coat Finish Paint | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 44 |
| L07-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 05-Sep-14 | 09-Sep-14 | 57 |
| L08-8110 | HVAC Trim / Finish | 5 | 5 | 05-Sep-14 | 11-Sep-14 | 52 |
| L09-8107 | Final Coat Finish Paint | 5 | 5 | 05-Sep-14 | 11-Sep-14 | 48 |
| L11-8128 | Install Tub Surrounds | 5 | 5 | 05-Sep-14 | 11-Sep-14 | 40 |
| L15-8102 | Hang GWB/Install Sound Batts | 4 | 4 | 05-Sep-14 | 10-Sep-14 | 0 |
| L08-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 52 |
| L09-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 48 |
| L10-8124 | Flooring | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 44 |
| L05-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 08-Sep-14 | 58 |
| L06-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 08-Sep-14 | 58 |

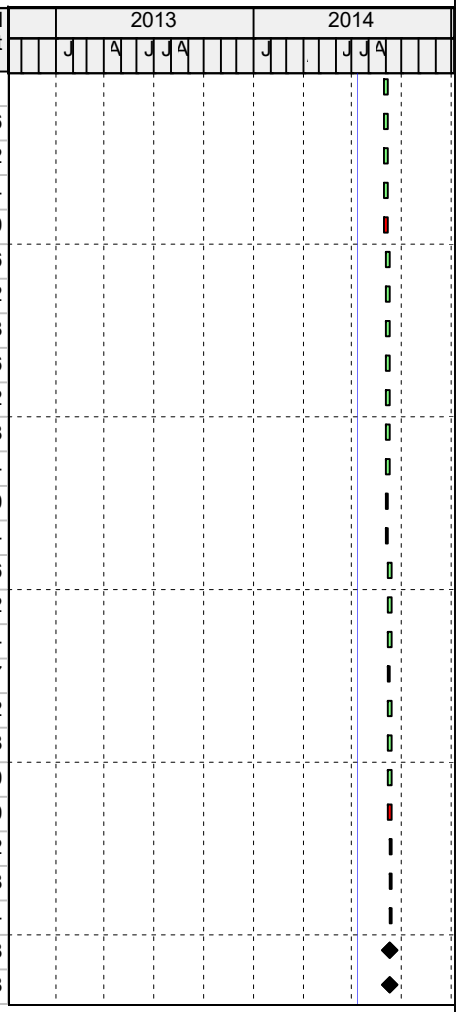


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 58 |
| L05-8134 | Pre-Clean Guestrooms | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 61 |
| L06-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 58 |
| L06-8134 | Pre-Clean Guestrooms | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 61 |
| L08-8126 | Doors & Hardware | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 52 |
| L09-8108 | Elec Trim / Finish | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 48 |
| L10-8116 | Install Wood Base | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 44 |
| L11-8120 | Install Bathroom Countertops | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 40 |
| L12-8104 | Primer Paint Coat | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 36 |
| L17-8102S | Stock GWB | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 4 |
| L08-8114 | Signage (By Owner) | 5 | 5 | 10-Sep-14 | 16-Sep-14 | 52 |
| L09-8118 | Elec Specialties Trim / Finish | 5 | 5 | 10-Sep-14 | 16-Sep-14 | 48 |
| L11-8105 | First Coat Finish Paint | 5 | 5 | 10-Sep-14 | 16-Sep-14 | 40 |
| L08-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 11-Sep-14 | 15-Sep-14 | 53 |
| L09-8110 | HVAC Trim / Finish | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 48 |
| L10-8107 | Final Coat Finish Paint | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 44 |
| L12-8128 | Install Tub Surrounds | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 36 |
| L16-8102 | Hang GWB/Install Sound Batts | 4 | 4 | 11-Sep-14 | 16-Sep-14 | 0 |
| L09-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 48 |
| L10-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 44 |
| L11-8124 | Flooring | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 40 |
| L09-8126 | Doors & Hardware | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 48 |
| L10-8108 | Elec Trim / Finish | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 44 |
| L11-8116 | Install Wood Base | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 40 |
| L12-8120 | Install Bathroom Countertops | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 36 |
| L14-8104 | Primer Paint Coat | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 32 |
| L09-8114 | Signage (By Owner) | 5 | 5 | 16-Sep-14 | 22-Sep-14 | 48 |

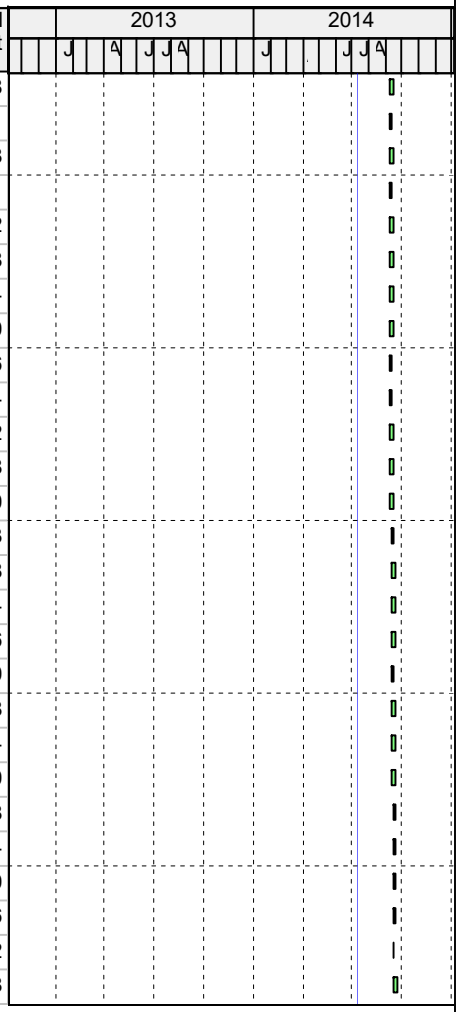



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8118 | Elec Specialties Trim / Finish | 5 | 5 | 16-Sep-14 | 22-Sep-14 | 44 |
| L12-8105 | First Coat Finish Paint | 5 | 5 | 16-Sep-14 | 22-Sep-14 | 36 |
| L07-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 16-Sep-14 | 52 |
| L08-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 16-Sep-14 | 52 |
| L07-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 52 |
| L07-8134 | Pre-Clean Guestrooms | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 55 |
| L08-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 52 |
| L08-8134 | Pre-Clean Guestrooms | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 55 |
| L09-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 17-Sep-14 | 19-Sep-14 | 49 |
| L10-8110 | HVAC Trim / Finish | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 44 |
| L11-8107 | Final Coat Finish Paint | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 40 |
| L14-8128 | Install Tub Surrounds | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 32 |
| L17-8102 | Hang GWB/Install Sound Batts | 6 | 6 | 17-Sep-14 | 24-Sep-14 | 0 |
| L10-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 44 |
| L11-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 40 |
| L12-8124 | Flooring | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 36 |
| L10-8126 | Doors & Hardware | 5 | 5 | 19-Sep-14 | 25-Sep-14 | 44 |
| L11-8108 | Elec Trim / Finish | 5 | 5 | 19-Sep-14 | 25-Sep-14 | 40 |
| L12-8116 | Install Wood Base | 5 | 5 | 19-Sep-14 | 25-Sep-14 | 36 |
| L14-8120 | Install Bathroom Countertops | 5 | 5 | 19-Sep-14 | 25-Sep-14 | 32 |
| L15-8104 | Primer Paint Coat | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 12 |
| L10-8114 | Signage (By Owner) | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 44 |
| L11-8118 | Elec Specialties Trim / Finish | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 40 |
| L14-8105 | First Coat Finish Paint | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 32 |
| L10-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 23-Sep-14 | 25-Sep-14 | 45 |
| L11-8110 | HVAC Trim / Finish | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 40 |
| L12-8107 | Final Coat Finish Paint | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 36 |

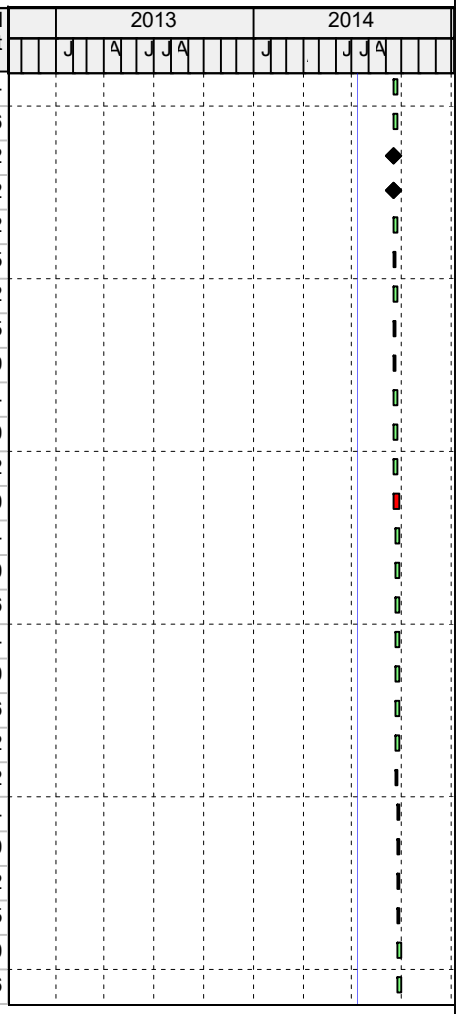



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8128 | Install Tub Surrounds | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 12 |
| L11-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 40 |
| L12-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 36 |
| L14-8124 | Flooring | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 32 |
| L09-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 24-Sep-14 | 46 |
| L09-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 46 |
| L09-8134 | Pre-Clean Guestrooms | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 49 |
| L11-8126 | Doors & Hardware | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 40 |
| L12-8108 | Elec Trim / Finish | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 36 |
| L14-8116 | Install Wood Base | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 32 |
| L15-8120 | Install Bathroom Countertops | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 12 |
| L16-8104 | Primer Paint Coat | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 8 |
| L11-8114 | Signage (By Owner) | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 40 |
| L12-8118 | Elec Specialties Trim / Finish | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 36 |
| L15-8105 | First Coat Finish Paint | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 12 |
| L10-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 26-Sep-14 | 44 |
| L10-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 44 |
| L10-8134 | Pre-Clean Guestrooms | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 47 |
| L11-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 29-Sep-14 | 01-Oct-14 | 41 |
| L12-8110 | HVAC Trim / Finish | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 36 |
| L14-8107 | Final Coat Finish Paint | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 32 |
| L16-8128 | Install Tub Surrounds | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 8 |
| L12-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 36 |
| L14-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 32 |
| L15-8124 | Flooring | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 12 |
| L12-8126 | Doors & Hardware | 5 | 5 | 01-Oct-14 | 07-Oct-14 | 36 |
| L14-8108 | Elec Trim / Finish | 5 | 5 | 01-Oct-14 | 07-Oct-14 | 32 |

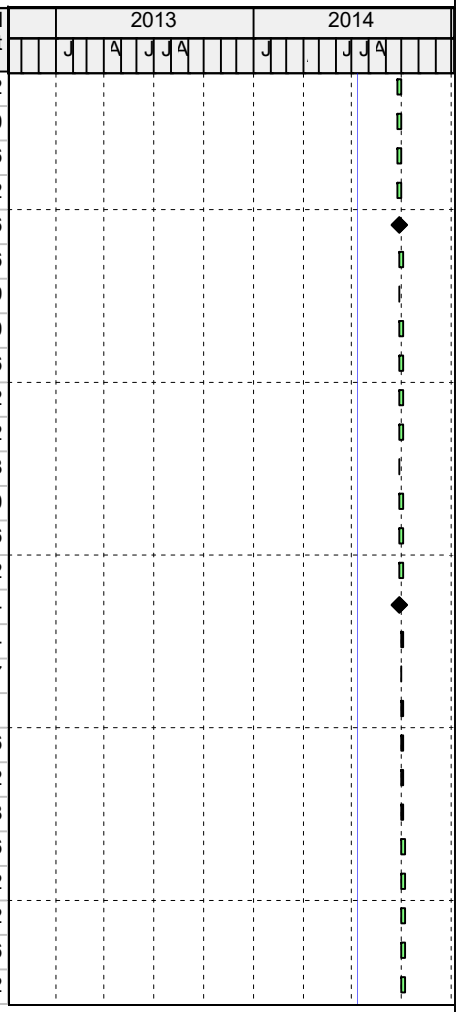



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8116 | Install Wood Base | 5 | 5 | 01-Oct-14 | 07-Oct-14 | 12 |
| L16-8120 | Install Bathroom Countertops | 5 | 5 | 01-Oct-14 | 07-Oct-14 | 8 |
| L12-8114 | Signage (By Owner) | 5 | 5 | 02-Oct-14 | 08-Oct-14 | 36 |
| L14-8118 | Elec Specialties Trim / Finish | 5 | 5 | 02-Oct-14 | 08-Oct-14 | 32 |
| L16-8105 | First Coat Finish Paint | 5 | 5 | 02-Oct-14 | 08-Oct-14 | 8 |
| L11-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 02-Oct-14 | 40 |
| L11-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 40 |
| L11-8134 | Pre-Clean Guestrooms | 2 | 2 | 03-Oct-14 | 06-Oct-14 | 43 |
| L12-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 03-Oct-14 | 07-Oct-14 | 55 |
| L14-8110 | HVAC Trim / Finish | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 32 |
| L15-8107 | Final Coat Finish Paint | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 12 |
| L14-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 32 |
| L15-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 12 |
| L16-8124 | Flooring | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 8 |
| L14-8126 | Doors & Hardware | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 32 |
| L15-8108 | Elec Trim / Finish | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 12 |
| L16-8116 | Install Wood Base | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 8 |
| L14-8114 | Signage (By Owner) | 5 | 5 | 08-Oct-14 | 14-Oct-14 | 32 |
| L15-8118 | Elec Specialties Trim / Finish | 5 | 5 | 08-Oct-14 | 14-Oct-14 | 12 |
| L17-8104 | Primer Paint Coat | 2 | 2 | 08-Oct-14 | 09-Oct-14 | 0 |
| L12-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 08-Oct-14 | 36 |
| L12-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 36 |
| L12-8134 | Pre-Clean Guestrooms | 2 | 2 | 09-Oct-14 | 10-Oct-14 | 39 |
| L14-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 09-Oct-14 | 13-Oct-14 | 33 |
| L15-8110 | HVAC Trim / Finish | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 12 |
| L16-8107 | Final Coat Finish Paint | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 8 |
| L15-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 12 |

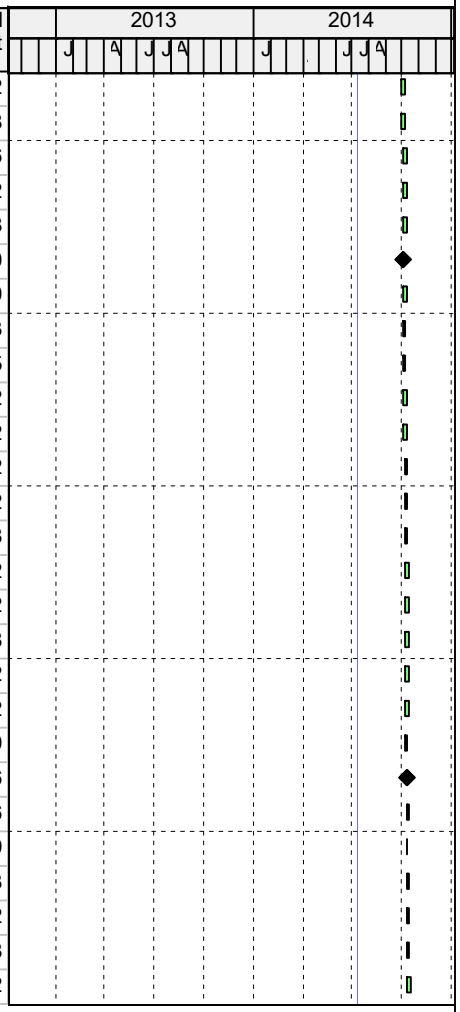



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 8 |
| L17-8128 | Install Tub Surrounds | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 0 |
| L15-8126 | Doors & Hardware | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 28 |
| L16-8108 | Elec Trim / Finish | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 8 |
| L15-8114 | Signage (By Owner) | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 28 |
| L16-8118 | Elec Specialties Trim / Finish | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 8 |
| L17-8120 | Install Bathroom Countertops | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 0 |
| L14-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 14-Oct-14 | 32 |
| L14-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 32 |
| L14-8134 | Pre-Clean Guestrooms | 2 | 2 | 15-Oct-14 | 16-Oct-14 | 35 |
| L15-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 15-Oct-14 | 17-Oct-14 | 29 |
| L16-8110 | HVAC Trim / Finish | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 8 |
| L17-8105 | First Coat Finish Paint | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 0 |
| L16-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 8 |
| L16-8126 | Doors & Hardware | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 24 |
| L17-8124 | Flooring | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 0 |
| L16-8114 | Signage (By Owner) | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 24 |
| L17-8116 | Install Wood Base | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 0 |
| L15-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 20-Oct-14 | 28 |
| L15-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 21-Oct-14 | 27-Oct-14 | 28 |
| L15-8134 | Pre-Clean Guestrooms | 2 | 2 | 21-Oct-14 | 22-Oct-14 | 31 |
| L16-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 25 |
| L17-8122 | Plumbing Fixtures & Trim / Finish | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 0 |
| L17-8107 | Final Coat Finish Paint | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 0 |
| L17-8108 | Elec Trim / Finish | 5 | 5 | 23-Oct-14 | 29-Oct-14 | 0 |
| L17-8118 | Elec Specialties Trim / Finish | 5 | 5 | 24-Oct-14 | 30-Oct-14 | 0 |
| L16-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 24-Oct-14 | 24 |

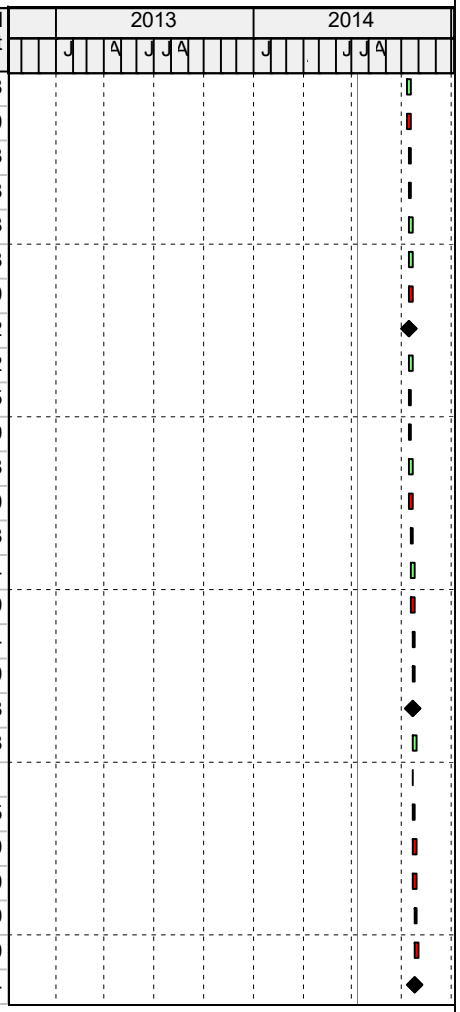



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 24 |
| L16-8134 | Pre-Clean Guestrooms | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 27 |
| L17-8110 | HVAC Trim / Finish | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 0 |
| L17-8112 | Fire Sprinkler Trim / Finish | 5 | 5 | 28-Oct-14 | 03-Nov-14 | 0 |
| L17-8126 | Doors & Hardware | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 16 |
| L17-8114 | Signage (By Owner) | 5 | 5 | 30-Oct-14 | 05-Nov-14 | 16 |
| L17-8109 | Acoustical Ceiling @ Corridors | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 16 |
| L17-8130 | Guest Rooms & Corridor Substantially Complete | 0 | 0 | | 05-Nov-14 | 16 |
| L17-8132 | Contractor Pre-Punchlist @ Guestrooms | 5 | 5 | 06-Nov-14 | 13-Nov-14 | 16 |
| L17-8134 | Pre-Clean Guestrooms | 2 | 2 | 06-Nov-14 | 07-Nov-14 | 19 |
| **Pool Area** | | | | | | |
| L03-8216 | L3 - Pool Surfaces / Finishes / Accessories | 16 | 16 | 15-Sep-14 | 06-Oct-14 | 41 |
| L03-8218 | L3 - Pool Equipment | 10 | 10 | 07-Oct-14 | 20-Oct-14 | 41 |
| **Corridors / Common / Public Areas** | | | | | | |
| L03-8200 | Vinyl Wall Coverings | 5 | 5 | 30-Jul-14 | 05-Aug-14 | 57 |
| L03-8206 | Flooring & Base @ Corridors | 2 | 2 | 04-Aug-14 | 05-Aug-14 | 74 |
| L04-8200 | Vinyl Wall Coverings | 5 | 5 | 04-Aug-14 | 08-Aug-14 | 54 |
| L04-8206 | Flooring & Base @ Corridors | 2 | 2 | 07-Aug-14 | 08-Aug-14 | 71 |
| L03-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 74 |
| L03-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 74 |
| L05-8200 | Vinyl Wall Coverings | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 48 |
| L04-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 13-Aug-14 | 14-Aug-14 | 71 |
| L04-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 13-Aug-14 | 14-Aug-14 | 71 |
| L05-8206 | Flooring & Base @ Corridors | 2 | 2 | 15-Aug-14 | 18-Aug-14 | 65 |
| L06-8200 | Vinyl Wall Coverings | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 60 |
| L05-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 65 |
| L05-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 65 |

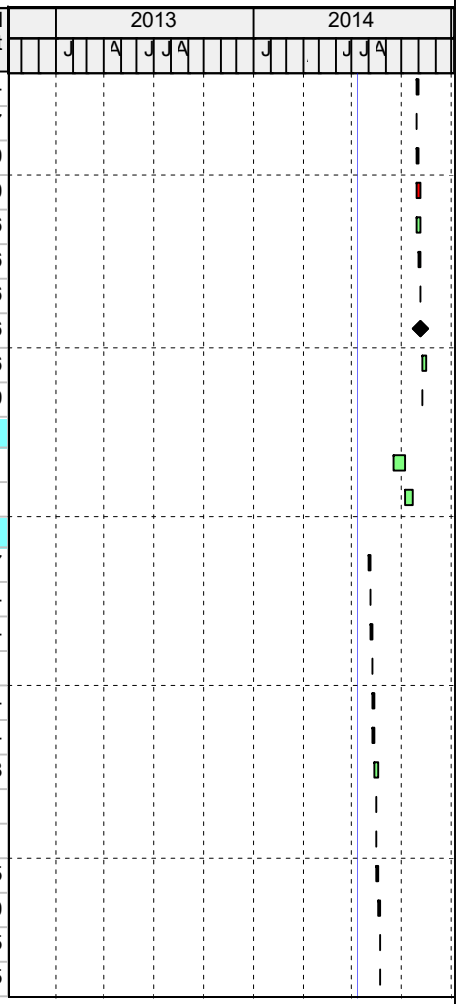


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8206 | Flooring & Base @ Corridors | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 61 |
| L07-8200 | Vinyl Wall Coverings | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 56 |
| L06-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 61 |
| L06-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 61 |
| L07-8206 | Flooring & Base @ Corridors | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 57 |
| L08-8200 | Vinyl Wall Coverings | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 52 |
| L07-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 03-Sep-14 | 04-Sep-14 | 57 |
| L07-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 03-Sep-14 | 04-Sep-14 | 57 |
| L08-8206 | Flooring & Base @ Corridors | 2 | 2 | 03-Sep-14 | 04-Sep-14 | 53 |
| L09-8200 | Vinyl Wall Coverings | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 48 |
| L03-8208 | Final Clean | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 64 |
| L04-8208 | Final Clean | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 64 |
| L08-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 53 |
| L08-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 53 |
| L09-8206 | Flooring & Base @ Corridors | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 49 |
| L03-8210 | Owner Walk / Create Punchlist | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 64 |
| L04-8210 | Owner Walk / Create Punchlist | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 64 |
| L10-8200 | Vinyl Wall Coverings | 5 | 5 | 10-Sep-14 | 16-Sep-14 | 44 |
| L03-8212 | Resolve Final Punchlist | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 64 |
| L04-8212 | Resolve Final Punchlist | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 64 |
| L09-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 49 |
| L09-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 49 |
| L10-8206 | Flooring & Base @ Corridors | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 45 |
| L05-8208 | Final Clean | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 58 |
| L06-8208 | Final Clean | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 58 |
| L11-8200 | Vinyl Wall Coverings | 5 | 5 | 16-Sep-14 | 22-Sep-14 | 40 |
| L04-8214 | Floor Complete | 0 | 0 | | 17-Sep-14 | 64 |

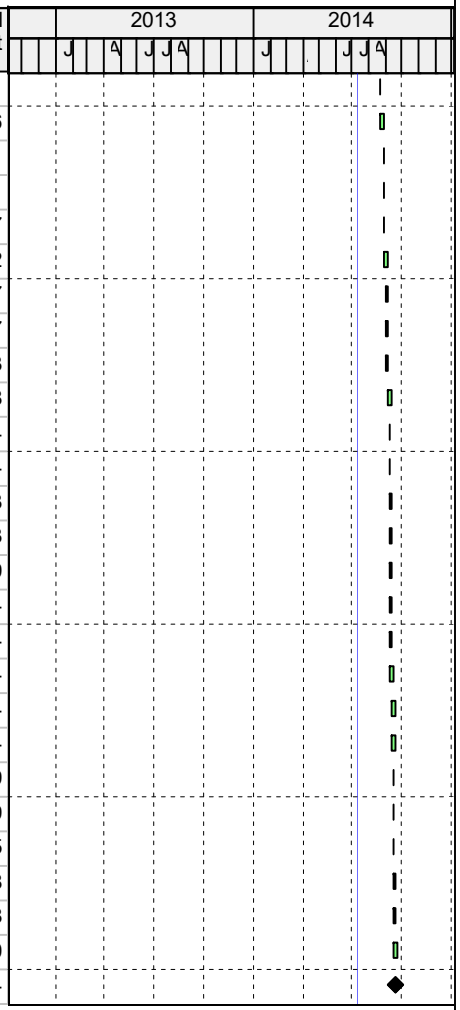



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8210 | Owner Walk / Create Punchlist | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 58 |
| L06-8210 | Owner Walk / Create Punchlist | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 58 |
| L05-8212 | Resolve Final Punchlist | 5 | 5 | 19-Sep-14 | 25-Sep-14 | 58 |
| L06-8212 | Resolve Final Punchlist | 5 | 5 | 19-Sep-14 | 25-Sep-14 | 58 |
| L10-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 45 |
| L10-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 45 |
| L11-8206 | Flooring & Base @ Corridors | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 41 |
| L12-8200 | Vinyl Wall Coverings | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 36 |
| L07-8208 | Final Clean | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 52 |
| L08-8208 | Final Clean | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 52 |
| L11-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 41 |
| L11-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 41 |
| L12-8206 | Flooring & Base @ Corridors | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 40 |
| L05-8214 | Floor Complete | 0 | 0 | | 25-Sep-14 | 58 |
| L06-8214 | Floor Complete | 0 | 0 | | 25-Sep-14 | 58 |
| L07-8210 | Owner Walk / Create Punchlist | 1 | 1 | 26-Sep-14 | 26-Sep-14 | 52 |
| L08-8210 | Owner Walk / Create Punchlist | 1 | 1 | 26-Sep-14 | 26-Sep-14 | 52 |
| L14-8200 | Vinyl Wall Coverings | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 32 |
| L07-8212 | Resolve Final Punchlist | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 52 |
| L08-8212 | Resolve Final Punchlist | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 52 |
| L12-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 01-Oct-14 | 02-Oct-14 | 40 |
| L12-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 01-Oct-14 | 02-Oct-14 | 40 |
| L14-8206 | Flooring & Base @ Corridors | 2 | 2 | 01-Oct-14 | 02-Oct-14 | 33 |
| L03-8214 | Floor Complete | 0 | 0 | | 01-Oct-14 | 54 |
| L09-8208 | Final Clean | 2 | 2 | 02-Oct-14 | 03-Oct-14 | 46 |
| L15-8200 | Vinyl Wall Coverings | 5 | 5 | 02-Oct-14 | 08-Oct-14 | 12 |
| L07-8214 | Floor Complete | 0 | 0 | | 03-Oct-14 | 52 |

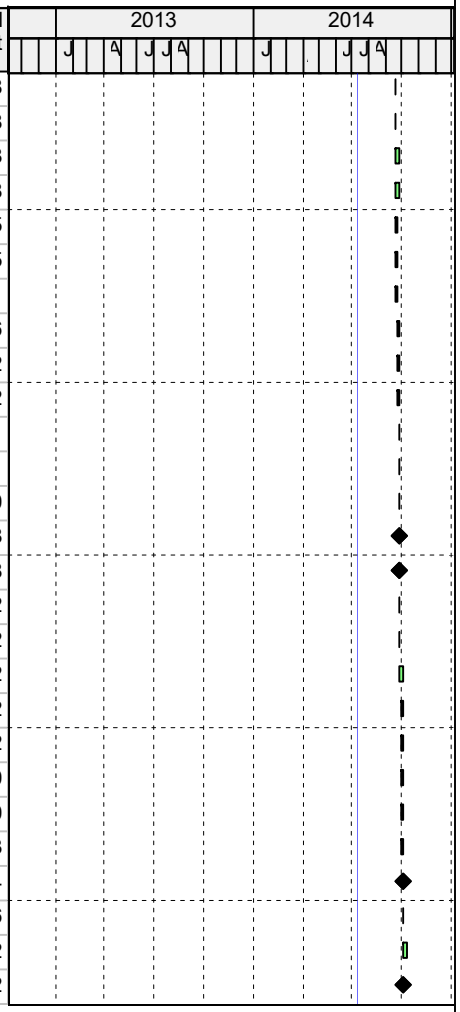



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8214 | Floor Complete | 0 | 0 | | 03-Oct-14 | 52 |
| L09-8210 | Owner Walk / Create Punchlist | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 46 |
| L10-8208 | Final Clean | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 44 |
| L09-8212 | Resolve Final Punchlist | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 46 |
| L14-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 33 |
| L14-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 33 |
| L15-8206 | Flooring & Base @ Corridors | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 29 |
| L10-8210 | Owner Walk / Create Punchlist | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 44 |
| L16-8200 | Vinyl Wall Coverings | 5 | 5 | 08-Oct-14 | 14-Oct-14 | 8 |
| L10-8212 | Resolve Final Punchlist | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 44 |
| L11-8208 | Final Clean | 2 | 2 | 10-Oct-14 | 13-Oct-14 | 40 |
| L15-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 13-Oct-14 | 14-Oct-14 | 29 |
| L15-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 13-Oct-14 | 14-Oct-14 | 29 |
| L16-8206 | Flooring & Base @ Corridors | 2 | 2 | 13-Oct-14 | 14-Oct-14 | 25 |
| L09-8214 | Floor Complete | 0 | 0 | | 13-Oct-14 | 46 |
| L11-8210 | Owner Walk / Create Punchlist | 1 | 1 | 14-Oct-14 | 14-Oct-14 | 40 |
| L11-8212 | Resolve Final Punchlist | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 40 |
| L10-8214 | Floor Complete | 0 | 0 | | 15-Oct-14 | 44 |
| L12-8208 | Final Clean | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 36 |
| L16-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 17-Oct-14 | 20-Oct-14 | 25 |
| L16-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 17-Oct-14 | 20-Oct-14 | 25 |
| L12-8210 | Owner Walk / Create Punchlist | 1 | 1 | 20-Oct-14 | 20-Oct-14 | 36 |
| L12-8212 | Resolve Final Punchlist | 5 | 5 | 21-Oct-14 | 27-Oct-14 | 36 |
| L17-8200 | Vinyl Wall Coverings | 5 | 5 | 21-Oct-14 | 27-Oct-14 | 0 |
| L11-8214 | Floor Complete | 0 | 0 | | 21-Oct-14 | 40 |
| L14-8208 | Final Clean | 2 | 2 | 22-Oct-14 | 23-Oct-14 | 32 |
| L14-8210 | Owner Walk / Create Punchlist | 1 | 1 | 24-Oct-14 | 24-Oct-14 | 32 |

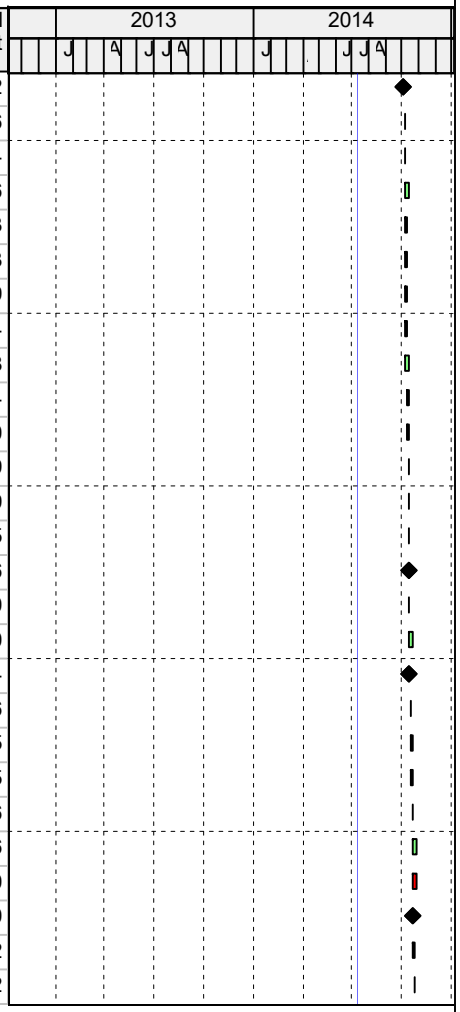


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8206 | Flooring & Base @ Corridors | 2 | 2 | 24-Oct-14 | 27-Oct-14 | 16 |
| L14-8212 | Resolve Final Punchlist | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 32 |
| L12-8214 | Floor Complete | 0 | 0 | | 27-Oct-14 | 36 |
| L15-8208 | Final Clean | 2 | 2 | 28-Oct-14 | 29-Oct-14 | 28 |
| L15-8210 | Owner Walk / Create Punchlist | 1 | 1 | 30-Oct-14 | 30-Oct-14 | 28 |
| L17-8202 | Elec Trim / Finish @ Corridors | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 16 |
| L17-8204 | Mech Trim / Finish @ Corridors (HVAC) | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 16 |
| L15-8212 | Resolve Final Punchlist | 5 | 5 | 31-Oct-14 | 06-Nov-14 | 28 |
| L14-8214 | Floor Complete | 0 | 0 | | 31-Oct-14 | 32 |
| L16-8208 | Final Clean | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 24 |
| L16-8210 | Owner Walk / Create Punchlist | 1 | 1 | 05-Nov-14 | 05-Nov-14 | 24 |
| L16-8212 | Resolve Final Punchlist | 5 | 5 | 06-Nov-14 | 13-Nov-14 | 24 |
| L15-8214 | Floor Complete | 0 | 0 | | 06-Nov-14 | 28 |
| L16-8214 | Floor Complete | 0 | 0 | | 13-Nov-14 | 24 |
| L17-8208 | Final Clean | 2 | 2 | 14-Nov-14 | 17-Nov-14 | 16 |
| L17-8210 | Owner Walk / Create Punchlist | 1 | 1 | 18-Nov-14 | 18-Nov-14 | 16 |
| L17-8212 | Resolve Final Punchlist | 5 | 5 | 19-Nov-14 | 25-Nov-14 | 16 |
| L17-8214 | Floor Complete | 0 | 0 | | 25-Nov-14 | 16 |
| **Mech Penthouse** | | | | | | |
| PH-8100 | PH - Insulation | 3 | 3 | 04-Sep-14 | 08-Sep-14 | 11 |
| PH-8102 | PH - GWB Hang / Tape / Finish - (Including Common | 10 | 10 | 09-Sep-14 | 22-Sep-14 | 11 |
| PH-8104 | PH - Int Painting | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 11 |
| PH-8122 | PH - Plumbing Trim / Finish | 10 | 10 | 29-Sep-14 | 10-Oct-14 | 11 |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 29 |
| PH-8114 | PH - Signage | 2 | 2 | 30-Sep-14 | 01-Oct-14 | 45 |
| PH-8108 | PH - Elec Trim / Finish | 10 | 10 | 13-Oct-14 | 24-Oct-14 | 11 |
| PH-8110 | PH - HVAC Trim / Finish | 10 | 10 | 13-Oct-14 | 24-Oct-14 | 15 |

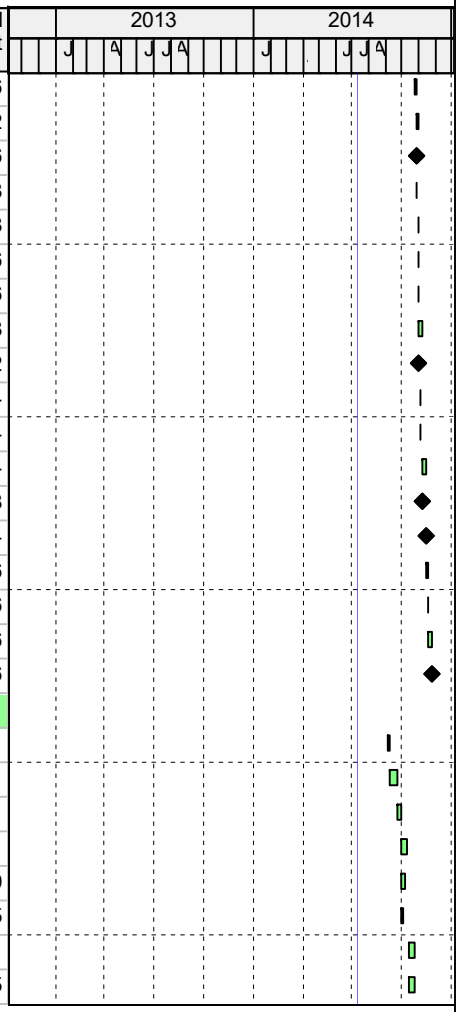



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-8118 | PH - Elec Specialties Trim / Finish | 4 | 4 | 27-Oct-14 | 30-Oct-14 | 11 |
| PH-8124 | PH - Flooring | 4 | 4 | 31-Oct-14 | 05-Nov-14 | 11 |
| PH-8126 | PH - Doors & Hardware | 3 | 3 | 04-Nov-14 | 06-Nov-14 | 11 |
| PH-8134 | PH - Pre-Clean | 3 | 3 | 07-Nov-14 | 12-Nov-14 | 11 |
| PH-8132 | PH - Contractor Pre-Punchlist | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 11 |
| PH-8208 | PH - Final Clean | 3 | 3 | 20-Nov-14 | 24-Nov-14 | 11 |
| PH-8210 | PH - Owner Walk / Create Punchlist | 1 | 1 | 25-Nov-14 | 25-Nov-14 | 11 |
| PH-8212 | PH - Final Punchlist | 5 | 5 | 26-Nov-14 | 04-Dec-14 | 11 |
| PH-8214 | PH - Floor Complete | 0 | 0 | | 04-Dec-14 | 11 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| Smoke Control | | | | | | |
| CO-7104 | Smoke Control Pre-Testing (Podium) | 5 | 5 | 25-Nov-14 | 03-Dec-14 | 7 |
| CO-7106 | City of Bellevue Smoke Control Testing (Podium) | 5 | 5 | 04-Dec-14 | 10-Dec-14 | 7 |
| CO-7108 | Final Marriott Smoke Control Testing | 5 | 5 | 11-Dec-14 | 17-Dec-14 | 7 |
| Fire Sprinklers | | | | | | |
| CO-7110 | Fire Sprinkler Pre-Testing (Podium) | 5 | 5 | 25-Nov-14 | 03-Dec-14 | 7 |
| CO-7112 | City of Bellevue Fire Sprinkler Inspection / Approval (F | 5 | 5 | 04-Dec-14 | 10-Dec-14 | 7 |
| CO-7114 | Marriott Fire Sprinkler Testing | 5 | 5 | 11-Dec-14 | 17-Dec-14 | 7 |
| Fire Alarm | | | | | | |
| CO-7116 | Fire Alarm Pre-Testing (Podium) | 5 | 5 | 25-Nov-14 | 03-Dec-14 | 7 |
| CO-7118 | City of Bellevue Fire Alarm Inspection / Approval (Pod | 5 | 5 | 04-Dec-14 | 10-Dec-14 | 7 |
| CO-7120 | Marriott Fire Alarm Testing | 5 | 5 | 11-Dec-14 | 17-Dec-14 | 7 |
| Start-Up / Testing / Commissioning | | | | | | |
| CO-7100 | CO - Preliminary Start-Up & Testing (Podium) | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 8 |
| CO-7102 | CO - HVAC Commissioning (Podium) | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 13 |

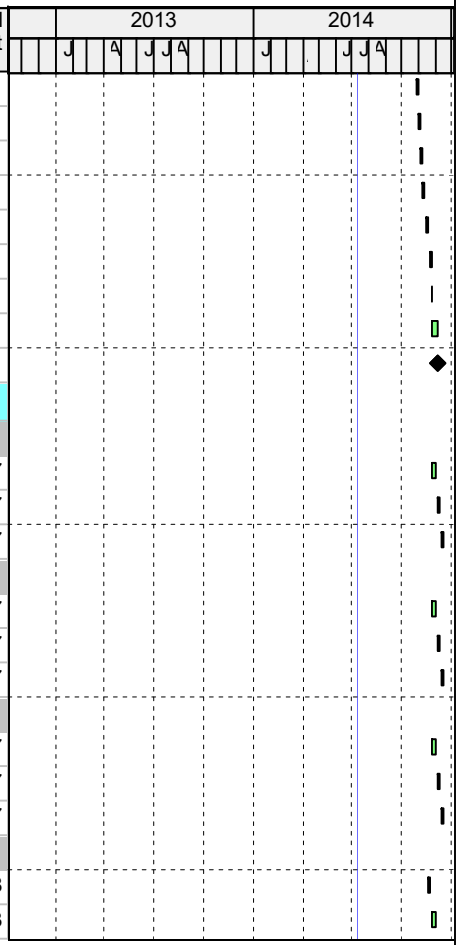



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Working Schedule - 8-7-14 Update** | | | | | | |
| I-1500 | Owner release revised LV design - Tower (ASIs 5, 13, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-1550 | Owner release revised LV design - Podium (ASIs 5, 1 | 200 | 0 | 23-May-13 A | 28-Apr-14 A | |
| I-1900 | Owner issue design revisions (ASIs 4, 9, 19, 34) | 215 | 0 | 23-May-13 A | 24-Mar-14 A | |
| I-2500 | Owner issue LL1 electrical revisions (ASIs 7, 9r2, 14, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-3400 | Owner provide Level 2 ceiling heights | 180 | 0 | 24-Jun-13 A | 24-Mar-14 A | |
| I-3700 | Owner resolve wall condition between stair and Eleva | 200 | 0 | 27-Jun-13 A | 16-Jun-14 A | |
| MM-1000 | MM - Temporary Power Available | 0 | 0 | 08-Jul-13 A | | |
| I-2100 | Owner revise roof steel design (Submittals 365, 370, | 200 | 0 | 09-Jul-13 A | 07-Apr-14 A | |
| I-2200 | Owner resolve elevator steel issue (RFI 112, RFI 112. | 200 | 0 | 09-Jul-13 A | 03-Mar-14 A | |
| I-2400 | Owner provide Tower light fixture selections (ASI 36) | 185 | 0 | 18-Jul-13 A | 08-Apr-14 A | |
| I-2900 | Owner revise Food Service and Kitchen (ASIs 11, 12, | 140 | 0 | 08-Aug-13 A | 27-Feb-14 A | |
| I-1400 | Owner develop envelope redesign | 70 | 0 | 27-Aug-13 A | 12-Dec-13 A | |
| I-3600 | Owner closeout glass/glazing allowance | 160 | 0 | 04-Sep-13 A | 30-Apr-14 A | |
| I-1200 | Owner release revised Concierge Lounge design (AS | 160 | 0 | 06-Sep-13 A | 08-Apr-14 A | |
| I-2800 | Owner revise interior public space design (ASIs 16, 1 | 130 | 0 | 25-Sep-13 A | 09-Apr-14 A | |
| I-2000 | Owner approve door frames (Submittals 258, 454, 48 | 85 | 0 | 27-Sep-13 A | 23-Jan-14 A | |
| I-3100 | Owner revise ballroom ceiling design (ASIs 18, 25) | 100 | 0 | 17-Oct-13 A | 25-Feb-14 A | |
| I-1600 | Owner provide directive for south & east corridor encl | 110 | 0 | 28-Oct-13 A | 18-Apr-14 A | |
| I-2300 | Owner resolve fire smoke dampers issue (RFI 233) | 115 | 0 | 30-Oct-13 A | 11-Apr-14 A | |
| I-2600 | Owner resolve L2 slab coordination issue | 4 | 0 | 13-Nov-13 A | 16-Nov-13 A | |
| I-2700 | Owner revise tower guest rooms design (ASIs 23, 29) | 58 | 0 | 04-Dec-13 A | 26-Feb-14 A | |
| I-1700 | Owner provide design for dry site utilities (ASIs 20, 20 | 66 | 0 | 09-Dec-13 A | 13-Mar-14 A | |
| I-1402 | Begin exterior panel production | 41 | 0 | 13-Dec-13 A | 12-Feb-14 A | |
| I-1300 | Owner issue "Hold" directive (email) | 0 | 0 | | 19-Dec-13 A | |
| I-1100 | Owner release revised L17 design (ASI 23, 29R1) | 74 | 0 | 20-Dec-13 A | 08-Apr-14 A | |
| I-1302 | Owner issue ASI 30 (Prep Kitchen Revisions) | 47 | 0 | 20-Dec-13 A | 27-Feb-14 A | |

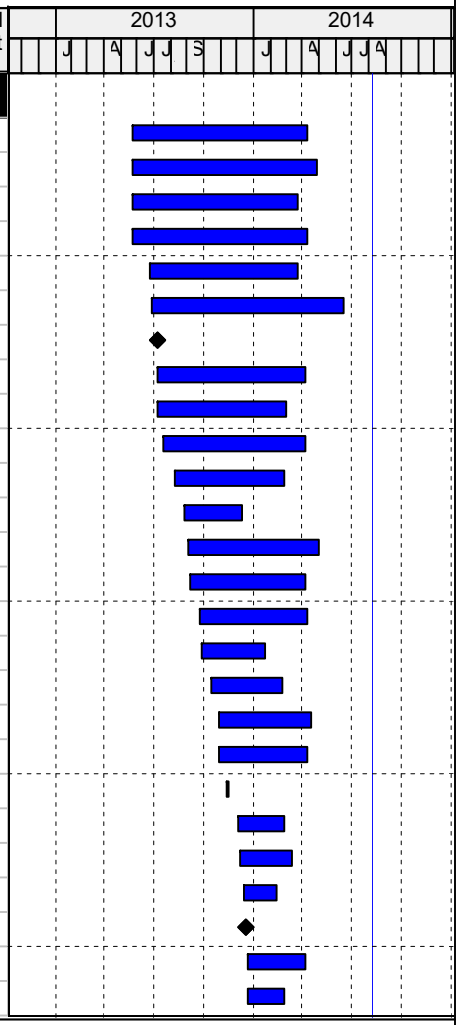


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| High Rise Hotel Sample Project | All Activities | Schedule Status Date 08-Aug-14 |
|---|---|---|

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1404 | City of Bellevue Approval | 90 | 0 | 23-Dec-13 A | 15-Jul-14 A | |
| I-3000 | Owner revise bar area (change to straight bar, IDRFI-( | 71 | 0 | 22-Jan-14 A | 27-May-14 A | |
| I-1306 | Prep Kitchen - Additional plumbing (ASI 30) | 4 | 0 | 17-Feb-14 A | 01-Aug-14 A | |
| I-2202 | Fabricate revised elevator steel | 60 | 0 | 04-Mar-14 A | 07-May-14 A | |
| I-2704 | Framing "Go Back" work for ASIs 23, 29 - L4 | 1 | 0 | 05-Mar-14 A | 12-Mar-14 A | |
| I-3900 | RFI 471, Resolve Ballroom parapet height issue | 1 | 0 | 08-Mar-14 A | 07-May-14 A | |
| I-1702 | Owner provide directive to proceed | 26 | 0 | 14-Mar-14 A | 01-May-14 A | |
| I-3300 | Owner provide Guest Room plumbing fixture selectio | 1 | 0 | 20-Mar-14 A | 20-Mar-14 A | |
| I-1902 | Procure revised structural steel | 15 | 0 | 25-Mar-14 A | 14-Apr-14 A | |
| I-4000 | Owner complete design of east stitched enclosure (fo | 1 | 0 | 01-Apr-14 A | 14-May-14 A | |
| I-2102 | Fabricate revised roof steel | 20 | 0 | 08-Apr-14 A | 15-May-14 A | |
| I-3200 | Owner provide light fixture selections for podium level | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| I-3800 | Resolve Heat Pump Electrical Overcurrent Issue | 20 | 0 | 23-Apr-14 A | 18-Jun-14 A | |
| L10-8221 | HVAC Risers Duct Insulation | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L11-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| I-2304 | Framing "Go Back" work at L3 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2306 | Framing "Go Back" work at L4 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2308 | Framing "Go Back" work at L5 for RFI 233 | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2706 | Framing "Go Back" work for ASIs 23, 29 - L5 | 1 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2708 | Framing "Go Back" work for ASIs 23, 29 - L6 | 1 | 0 | 29-Apr-14 A | 09-May-14 A | |
| I-2702 | Framing "Go Back" work for ASIs 23, 29 - L3 | 1 | 0 | 01-May-14 A | 01-May-14 A | |
| I-1706 | PSE scheduling delay | 10 | 0 | 01-May-14 A | 20-May-14 A | |
| I-3602 | Complete shop drawings & fab/deliver storefront fram | 40 | 0 | 01-May-14 A | 14-Jun-14 A | |
| L04-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| I-1802 | Rework framing for door hold-opens - LL4 | 1 | 0 | 07-May-14 A | 08-May-14 A | |
| L04-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-May-14 A | 12-May-14 A | |

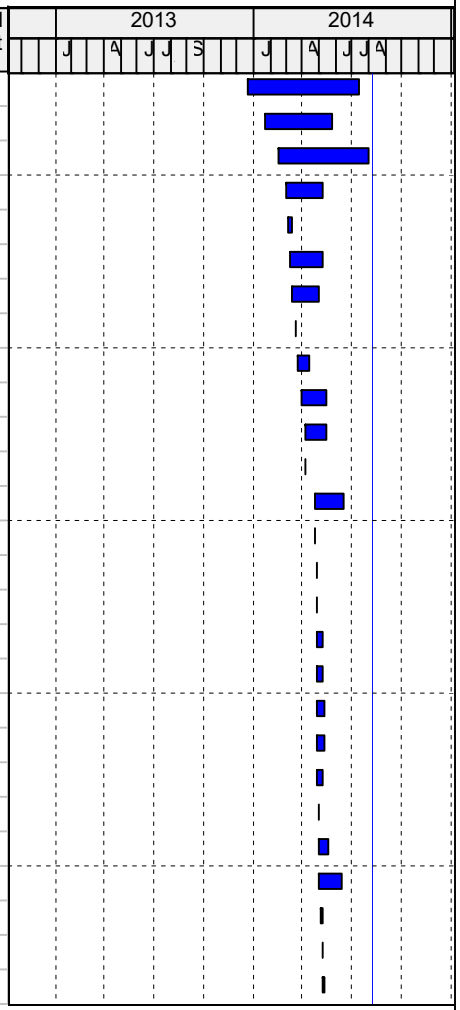



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1800 | Owner issue directive to proceed with door hold-open | 1 | 0 | 08-May-14 A | 08-May-14 A | |
| I-1804 | Rework framing for door hold-opens - LL3 | 1 | 0 | 08-May-14 A | 09-May-14 A | |
| I-2312 | Framing "Go Back" work at L7 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-2314 | Framing "Go Back" work at L8 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-3902 | Install Ballroom parapet extension | 5 | 0 | 08-May-14 A | 13-May-14 A | |
| I-1806 | Rework framing for door hold-opens - LL2 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-1808 | Rework framing for door hold-opens - LL1 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-2310 | Framing "Go Back" work at L6 for RFI 233 | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| I-2710 | Framing "Go Back" work for ASIs 23, 29 - L7 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| L05-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L06-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L05-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| LL2E-8110 | LL2 - Electrical, Fire pumps/equipment final connectic | 5 | 2 | 12-May-14 A | 18-Aug-14 | 64 |
| PH-8704 | PH - Install Machine Support Steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| PH-8710 | Install elevator rail support steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| L03-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L03-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 13-May-14 A | 14-May-14 A | |
| I-4002 | East Stitched - Install framing and windows | 9 | 0 | 19-May-14 A | 09-Jun-14 A | |
| L10-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L11-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L12-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| RF-4038 | AR - Concrete pads and curbs | 5 | 0 | 21-May-14 A | 04-Jun-14 A | |
| L10-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L11-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L12-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L14-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |

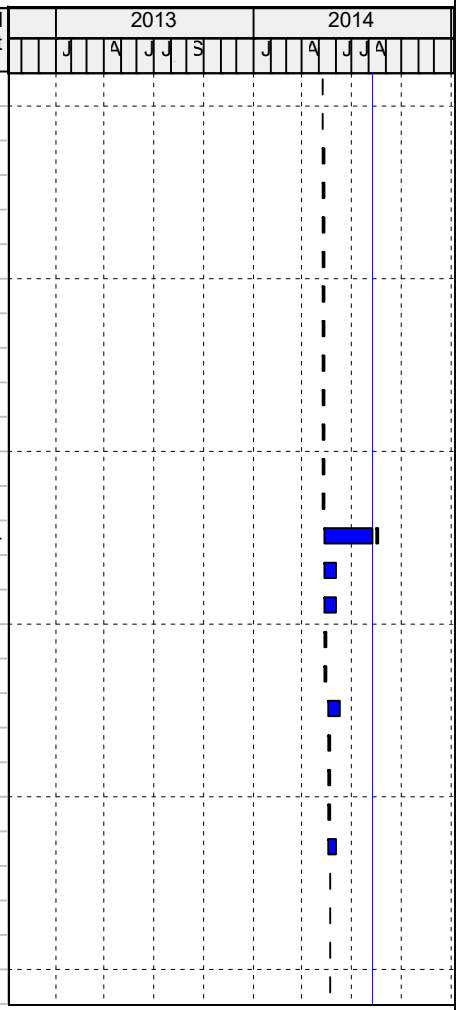



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 27-May-14 A | |
| L11-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 07-Jun-14 A | |
| L12-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 27-May-14 A | 06-Jun-14 A | |
| I-3002 | City of Bellevue approve bar design changes. | 5 | 2 | 28-May-14 A | 11-Aug-14 | 17 |
| L16-8221 | HVAC Risers Duct Insulation | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| PH-8712 | PH - Complete Framing and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| PH-8714 | Stage PH/L18 roofing materials | 2 | 0 | 30-May-14 A | 30-May-14 A | |
| L08-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L08-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 02-Jun-14 A | 20-Jun-14 A | |
| PH-8704I | Correct support steel embeds | 2 | 0 | 02-Jun-14 A | 11-Jun-14 A | |
| L14-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 03-Jun-14 A | 04-Jun-14 A | |
| L17-8221 | HVAC Risers Duct Insulation | 1 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| PC-4010 | PC - Fireproof Entry Roof Steel | 5 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| I-4100 | Owner resolve trap primers issue (RFI 560) | 5 | 0 | 03-Jun-14 A | 20-Jun-14 A | |
| RF-6028 | Tower Roof - Structural Steel | 5 | 0 | 04-Jun-14 A | 17-Jun-14 A | |
| L14-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L1B-6005 | Head of Wall Fire Caulk at CMU (including East Servi | 2 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L14-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L15-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L16-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |

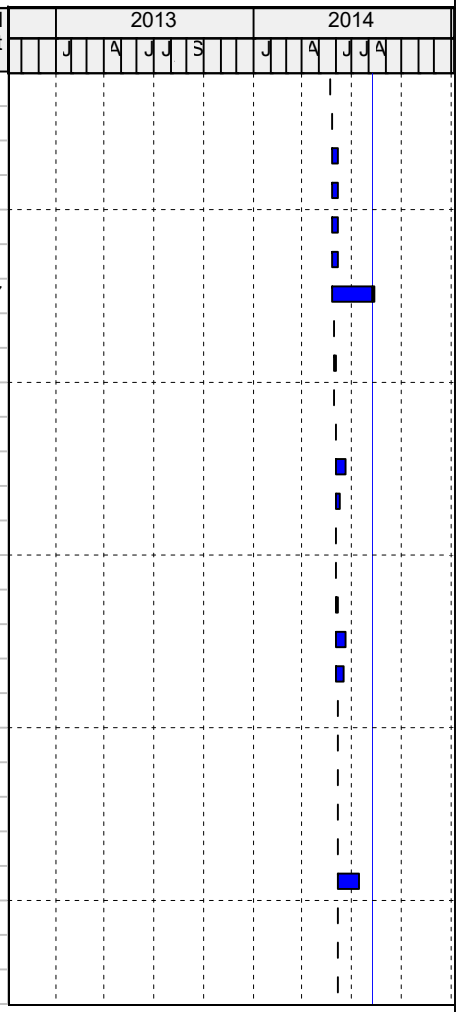



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 11-Jun-14 A | 12-Jun-14 A | |
| I-3702 | Complete wall framing at Stair/Elevator 5 (LL4) | 2 | 0 | 18-Jun-14 A | 20-Jun-14 A | |
| I-3720 | Fireproof added steel between Stair 1 and Elevator 5 | 5 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| I-3722 | Complete GWB between Stair 1 and Elevator 5 shaft | 10 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| LL1-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 22-Jul-14 A | |
| TC-5912 | Tower Crane pour-backs (LL4 to L3) | 4 | 0 | 19-Jun-14 A | 26-Jun-14 A | |
| LL1-Z2-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL4-6005 | LL4 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| LL3-6005 | LL3 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| L03-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 21-Jun-14 A | 21-Jun-14 A | |
| L06-6040 | Test Heat Pumps - L3, L4, L5 and L6 | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L03-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| L17-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL2-6005 | LL2 - Seismic Head Of Wall Fire Caulk at CMU | 5 | 0 | 24-Jun-14 A | 18-Jul-14 A | |
| I-3704 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL1-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z2-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z3-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 04-Aug-14 A | |
| L1L-6005 | Head of Wall Fire Caulk at CMU (including back of ho | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1K-6005 | Head of Wall Fire Caulk at CMU & Inspection | 2 | 1 | 24-Jun-14 A | 08-Aug-14 | 23 |
| L03-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L04-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| I-3710 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| I-3712 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| L1K-6018a | Install Kitchen hoods and grease ducts (OFCI) | 10 | 6 | 25-Jun-14 A | 26-Aug-14 | 30 |
| L03-8604 | L3 Pool - Plumbing R/I | 5 | 4 | 25-Jun-14 A | 14-Aug-14 | 57 |

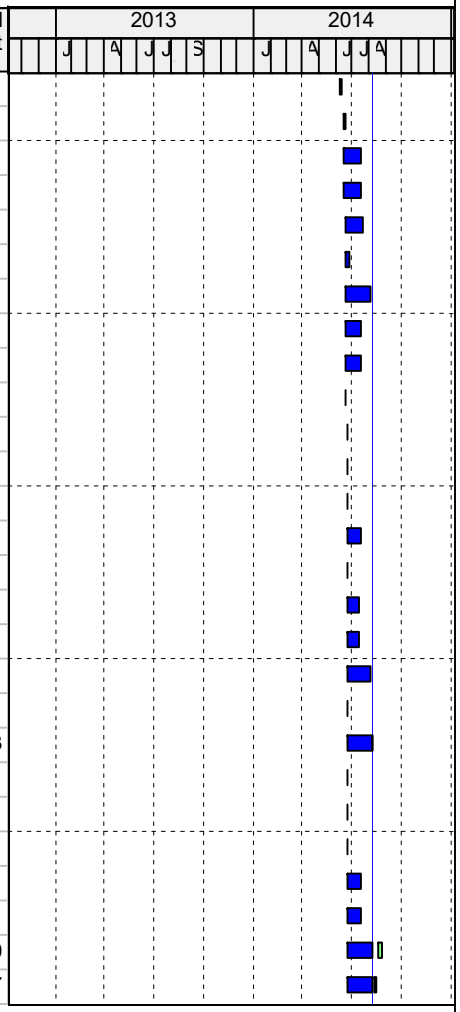



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 26-Jun-14 A | 03-Jul-14 A | |
| L09-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 26-Jun-14 A | 26-Jun-14 A | |
| I-3706 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 26-Jun-14 A | 10-Jul-14 A | |
| L03-8600 | L3 Pool - Framing & HM frames | 5 | 1 | 26-Jun-14 A | 08-Aug-14 | 56 |
| L05-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L08-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L04-7018 | Electrical Rough-In | 1 | 0 | 27-Jun-14 A | 22-Jul-14 A | |
| L04-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 27-Jun-14 A | 23-Jul-14 A | |
| L03-7020 | HVAC Rough-In | 1 | 0 | 29-Jun-14 A | 15-Jul-14 A | |
| L1RR-8100 | Insulation [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8100 | Insulation [DELETED - included in Ballroom activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8100 | Insulation [DELETED - included in Meeting Rooms ac | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8102 | GWB Hang [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8215 | GWB Tape [DELETED - included in Meeting Rooms a | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8104 | Prime Paint [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8102 | GWB Hang [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8215 | GWB Tape [DELETED - included in Ballroom activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8104 | Prime Paint [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8102 | GWB Hang [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |

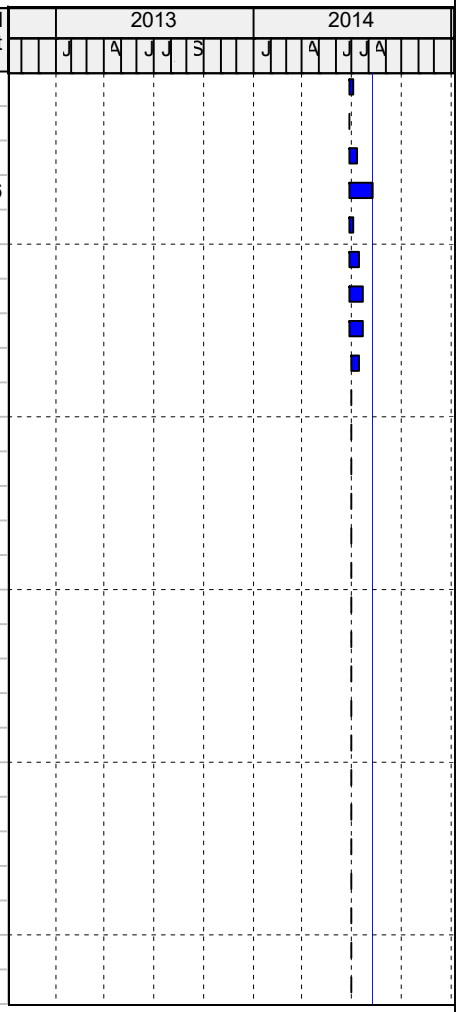


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1RR-8215 | GWB Tape [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8104 | Prime Paint [DELETED - included in Kitchen activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L03-7018 | Electrical Rough-In | 1 | 0 | 01-Jul-14 A | 14-Jul-14 A | |
| L03-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Jul-14 A | 15-Jul-14 A | |
| L10-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7102 | Install Vertical Heat Pump | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L03-7116 | Frame Walls | 1 | 0 | 02-Jul-14 A | 14-Jul-14 A | |
| L03-7118 | Install HM Door Frame | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L04-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L05-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L07-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L08-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L09-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L10-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L12-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| I-3708 | Complete wall framing at Stair/Elevator 5 (LL3) | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |

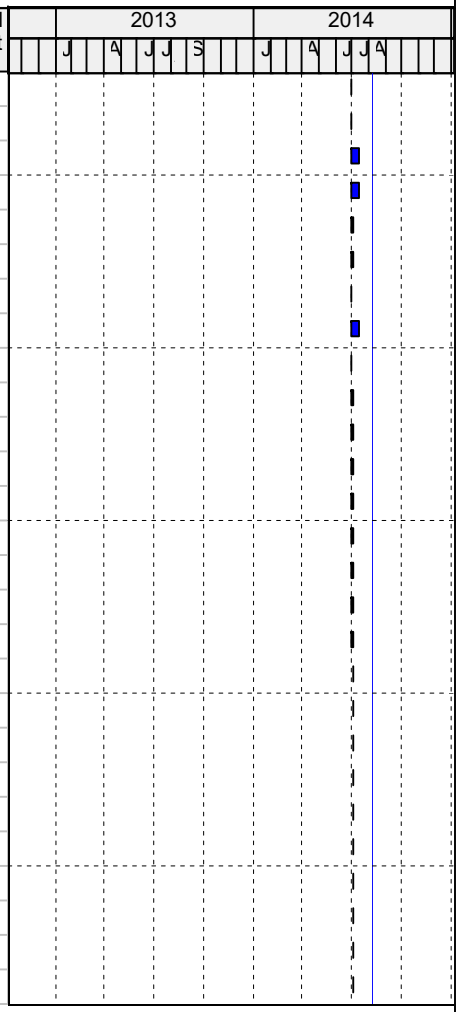



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 03-Jul-14 A | 07-Jul-14 A | |
| L04-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L05-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L06-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L07-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L08-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L17-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L10-6040 | Test Heat Pumps - L7, L8, L9 and L10 | 3 | 0 | 07-Jul-14 A | 09-Jul-14 A | |
| L10-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L03-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L04-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L05-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L06-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L07-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L08-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L09-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L10-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L12-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L14-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |

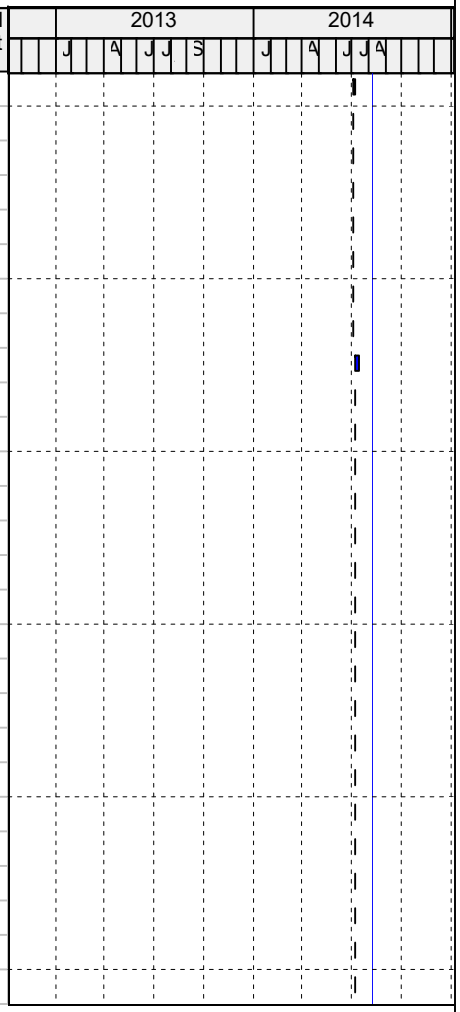



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Jul-14 A | 29-Jul-14 A | |
| L03-8602 | L3 Pool - Fire Sprinkler R/I | 5 | 0 | 08-Jul-14 A | 22-Jul-14 A | |
| L03-7016 | Install HM door frame | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L11-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L16-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 09-Jul-14 A | |
| L04-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |

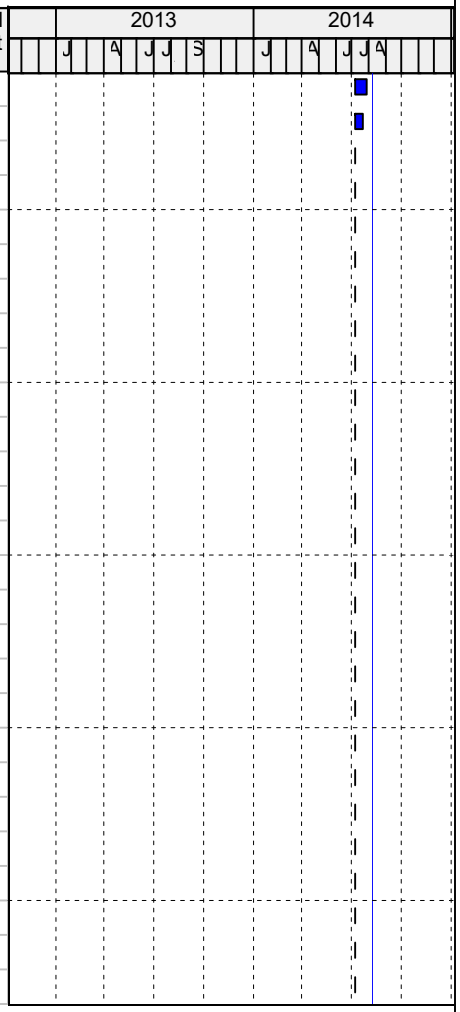



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L12-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| MP-FAB1 | Fabricate and Deliver Bronze Gold Horizontal Panels | 30 | 0 | 09-Jul-14 A | 15-Jul-14 A | |
| L04-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L05-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L06-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L16-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| MP-FAB2 | Fabricate and Deliver Silver Vertical Panels | 45 | 0 | 10-Jul-14 A | 08-Aug-14 | 61 |
| L07-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| LL2-2046 | LL2 - Generator Room build-out | 20 | 8 | 14-Jul-14 A | 19-Aug-14 | 70 |
| LL1-Z2-6018a | Complete Mech RI at tower crane opening (LL1) | 4 | 0 | 14-Jul-14 A | 17-Jul-14 A | |
| L08-6223 | Frame Corridor Ceilings | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| SW-2006a | Complete Dry Utilities (Phase 2) | 5 | 0 | 14-Jul-14 A | 24-Jul-14 A | |
| L04-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L04-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L05-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L06-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |

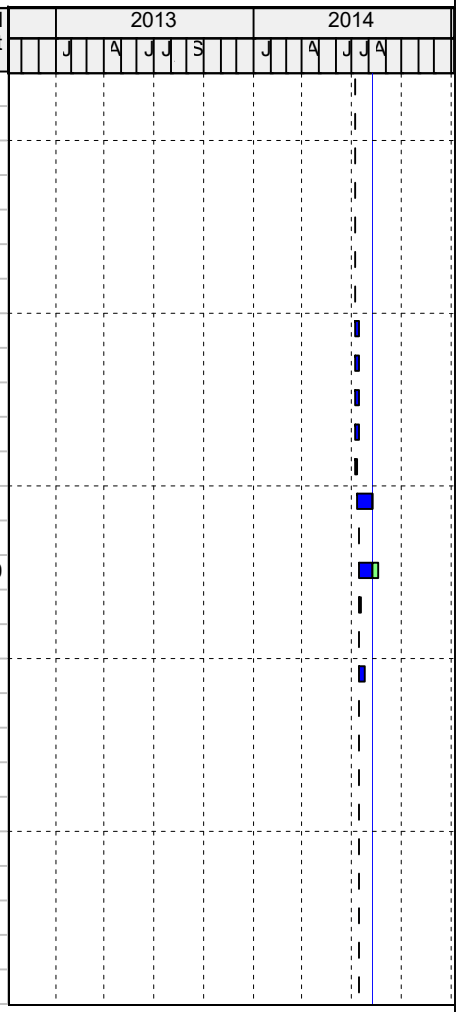



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L04-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L11-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L11-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L12-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L12-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L15-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L15-7102 | Install Vertical Heat Pump | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L1B-6026 | Install operable partition track | 2 | 1 | 15-Jul-14 A | 08-Aug-14 | 13 |
| L09-6223 | Frame corridor ceilings | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L03-7120 | Electrical Rough-In | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L07-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L07-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |

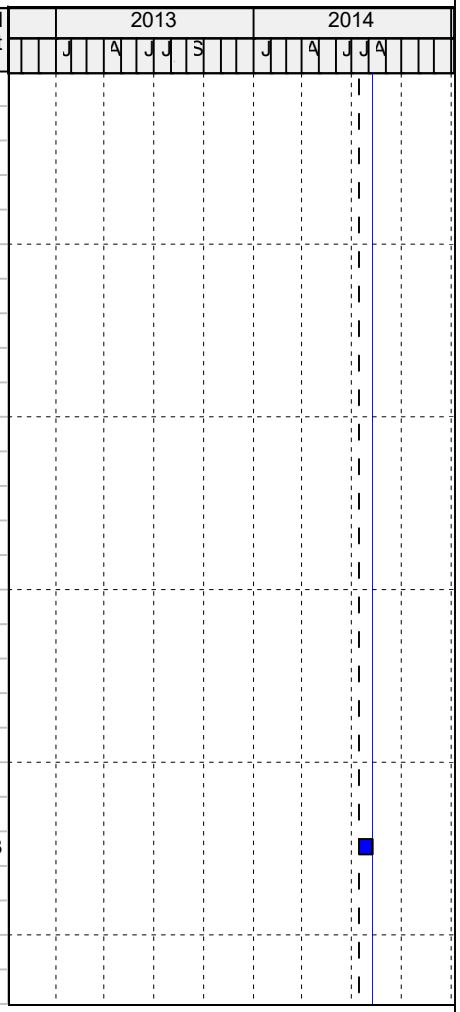



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L08-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L09-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L09-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L03-7142 | Install Laundry Chute (All Levels) | 9 | 0 | 15-Jul-14 A | 25-Jul-14 A | |
| LL2-2045 | LL2 - Electrical Room build-out | 15 | 5 | 15-Jul-14 A | 14-Aug-14 | 57 |
| MPT-1000 | Tower - Install Elevations 26-28 (west elevation) | 13 | 0 | 16-Jul-14 A | 01-Aug-14 A | |
| L03-7122 | HVAC Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L04-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L05-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L06-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L07-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L07-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L08-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L08-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L09-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L09-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |

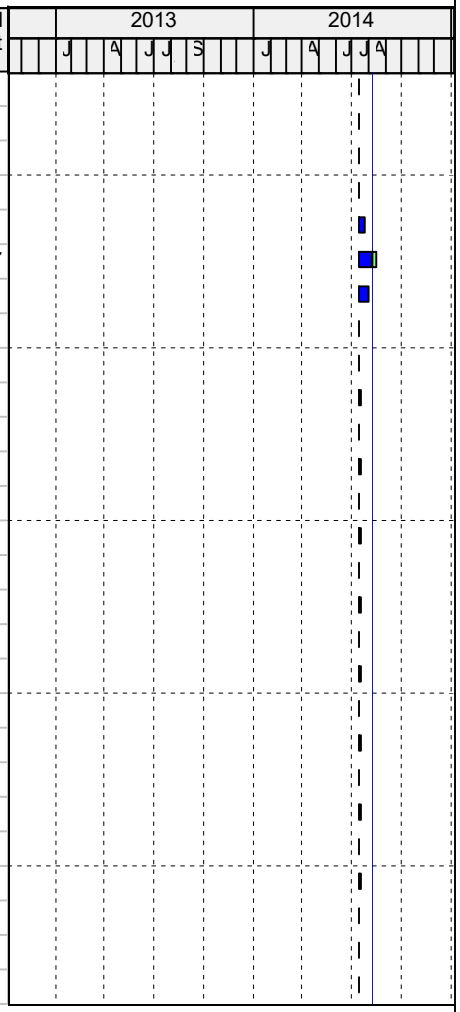



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L11-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L11-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L12-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L12-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L15-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L15-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L16-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L17-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L04-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L04-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L05-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L05-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L06-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L06-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L07-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L08-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L09-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |

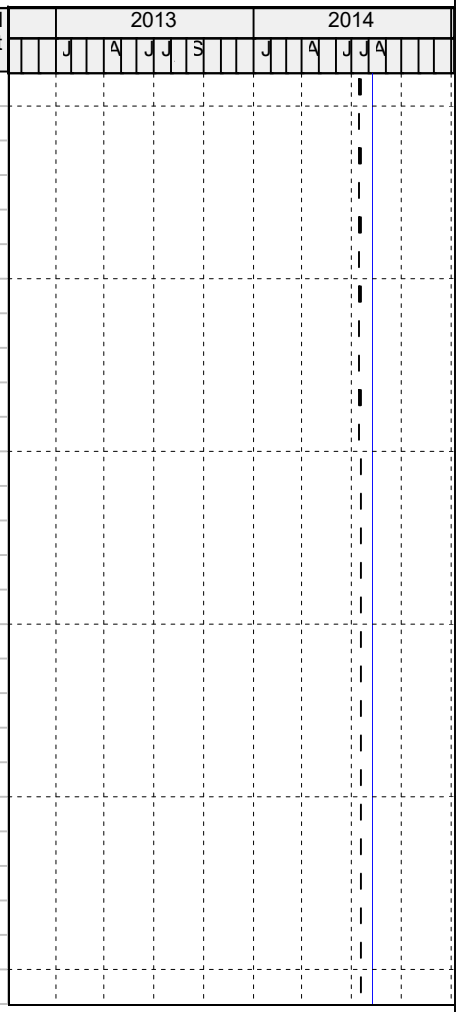



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L11-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L11-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L12-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L12-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L16-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L03-8608 | L3 Pool - Electrical R/I | 5 | 4 | 18-Jul-14 A | 14-Aug-14 | 57 |
| L03-8610 | L3 Pool - Fire Alarm / Elec Specialties R/I | 5 | 4 | 18-Jul-14 A | 14-Aug-14 | 57 |
| L15-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L15-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| L17-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L17-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| LL2-2052 | LL2 - Install fuel piping and exhaust duct to Generatc | 4 | 2 | 21-Jul-14 A | 11-Aug-14 | 34 |
| L04-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L04-7016 | Install HM door frame | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L07-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L08-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L10-7116 | Frame Walls | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L16-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 21-Jul-14 A | 22-Jul-14 A | |
| L16-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L17-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |

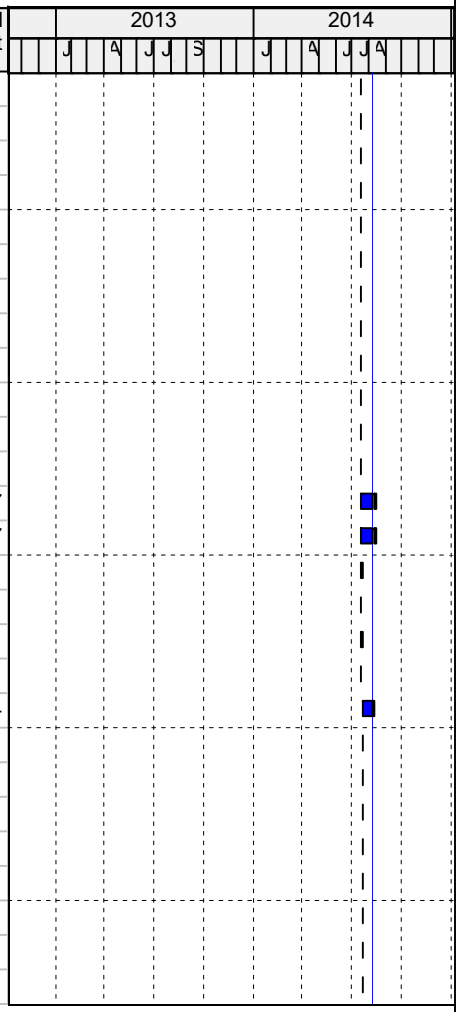



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPT-1002 | Tower - Install Elevation 35 (east elevation-south half) | 8 | 0 | 25-Jul-14 A | 06-Aug-14 A | |
| L16-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 25-Jul-14 A | 25-Jul-14 A | |
| MPT-1004 | Tower - Install Elevation 36a (east return L3-L17) | 6 | 0 | 28-Jul-14 A | 04-Aug-14 A | |
| L11-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L14-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L15-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L16-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L10-6223 | Frame Corridor Ceilings | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L11-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L15-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L15-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L11-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L14-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L16-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| I-1304 | Prep Kitchen - Additional framing (ASI 30) | 2 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-2302 | Framing "Go Back" work at LL1 for RFI 233 | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| I-2502 | Electrical rework at LL1 for ASIs 7, 9r2, 14, 27 | 4 | 1 | 01-Aug-14 A | 08-Aug-14 | 32 |
| L12-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L1B-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 5 | 01-Aug-14 A | 15-Aug-14 | 8 |
| L09-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |

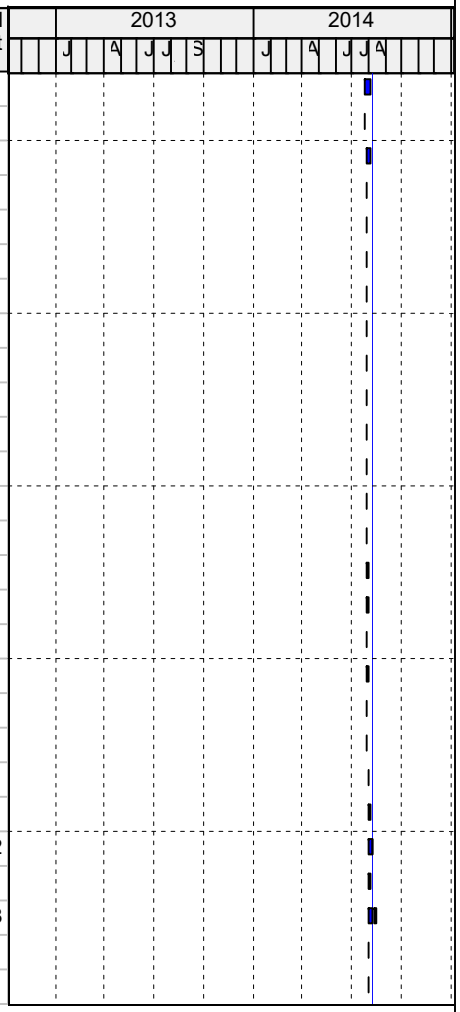



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L11-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L11-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L15-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L14-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L17-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L16-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 04-Aug-14 A | 05-Aug-14 A | |
| L04-7020 | HVAC Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L14-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L15-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 05-Aug-14 A | 07-Aug-14 A | |
| MPT-1006 | Tower - Install Elevation 40 (east return-east end) | 3 | 0 | 05-Aug-14 A | 07-Aug-14 A | |

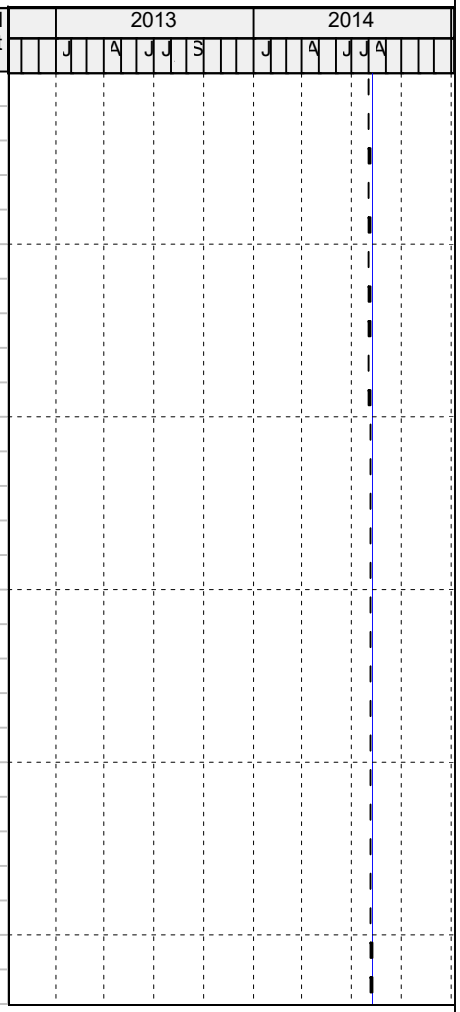



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L06-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L07-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L08-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L09-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L10-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7018 | Electrical Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L14-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 05-Aug-14 A | 06-Aug-14 A | |
| L14-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L05-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L06-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L07-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L08-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L09-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L10-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7020 | HVAC Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L16-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-6223 | Frame Corridor Ceilings | 4 | 1 | 07-Aug-14 A | 08-Aug-14 | 25 |
| EL-1220 | Elevator fronts delivered | 0 | 0 | 07-Aug-14 A | | |
| L12-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 28 |

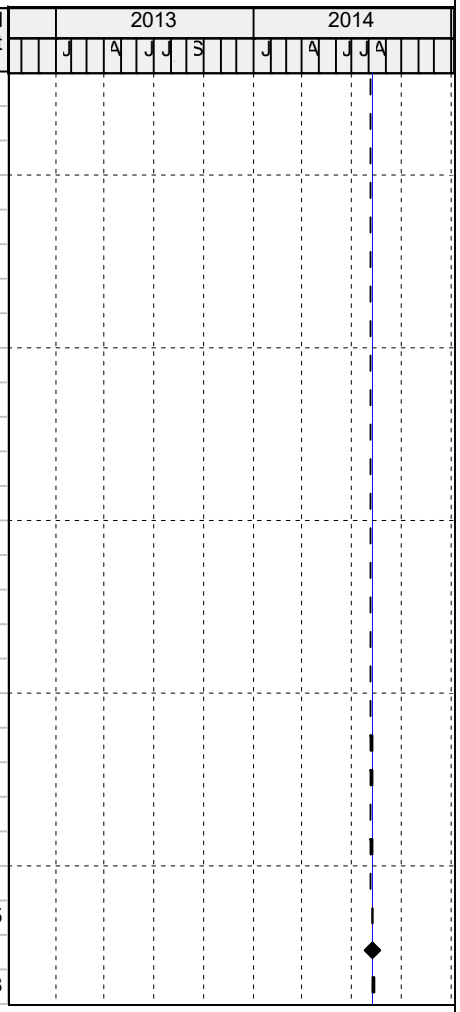



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 31 |
| L15-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 96 |
| L14-6040 | Test Heat Pumps - L11, L12 and L14 | 3 | 3 | 08-Aug-14 | 12-Aug-14 | 25 |
| L14-6036 | Framing Around Heat Pump & Soffit | 3 | 3 | 08-Aug-14 | 12-Aug-14 | 29 |
| L12-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 29 |
| L15-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 36 |
| LL2-2048 | LL2 - Set Laundry Room equipment (BY OTHERS) | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 78 |
| LL2E-8108 | LL2 - Set fire pumps and equipment | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 64 |
| MPT-1008 | Tower - Install Elevation 50 (roof, GL 14.5)) | 3 | 3 | 08-Aug-14 | 12-Aug-14 | 61 |
| MPT-1010 | Tower - Install Elevations 51-53 (north elevation, west | 7 | 7 | 08-Aug-14 | 18-Aug-14 | 61 |
| L04-6005 | CMU Fire Caulk/Clips | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 21 |
| I-4102 | Install added trap primers - LL2 | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 30 |
| I-4104 | Install added trap primers - LL1 | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 24 |
| I-4106 | Install added trap primers - L1 | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 13 |
| I-4108 | Install added trap primers - L2 | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 38 |
| I-4110 | Install added trap primers - L3 | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 19 |
| I-4112 | Install added trap primers - Roof PH | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 33 |
| L12-6223 | Frame Corridor Ceilings | 4 | 4 | 08-Aug-14 | 12-Aug-14 | 24 |
| L03-7026 | Inspections for GWB Cover | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 58 |
| L03-7128 | Inspections for GWB Cover | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 64 |
| L04-7026 | Inspections for GWB Cover | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 58 |
| L05-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 57 |
| L05-7016 | Install HM door frame | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 57 |
| L06-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 57 |
| L06-7016 | Install HM door frame | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 57 |
| L07-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 57 |
| L07-7016 | Install HM door frame | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 57 |

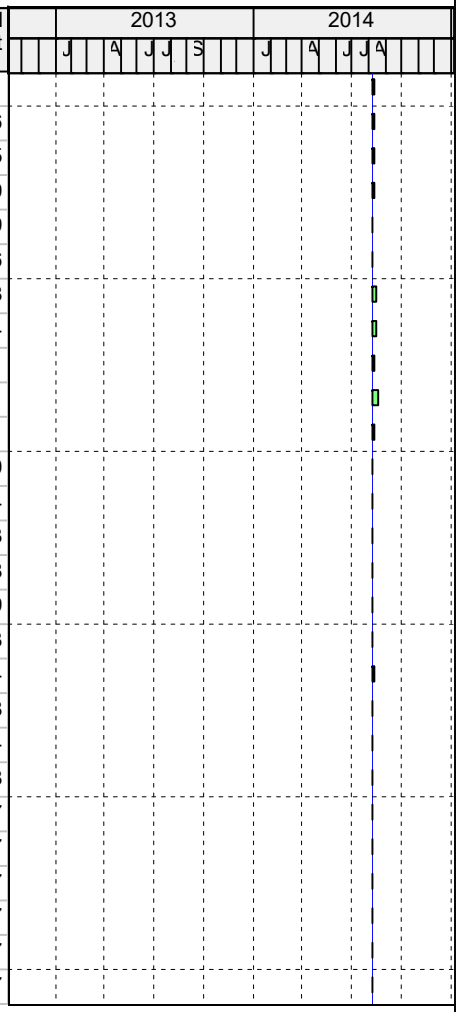



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 57 |
| L08-7016 | Install HM door frame | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 57 |
| L09-7026 | Inspections for GWB Cover | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 58 |
| L11-7016 | Install HM door frame | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 57 |
| L12-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 52 |
| L12-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 53 |
| L14-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 52 |
| L14-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 53 |
| L15-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 52 |
| L15-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 53 |
| L16-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 53 |
| L16-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 54 |
| L17-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 49 |
| L17-7004 | HVAC Firestop & Inspect (1) | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 50 |
| L04-7120 | Electrical Rough-In | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 62 |
| L05-7120 | Electrical Rough-In | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 62 |
| L06-7120 | Electrical Rough-In | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 62 |
| L07-7120 | Electrical Rough-In | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 62 |
| L08-7120 | Electrical Rough-In | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 62 |
| L09-7118 | Install HM Door Frame | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 63 |
| L09-7120 | Electrical Rough-In | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 61 |
| L10-7118 | Install HM Door Frame | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 63 |
| L10-7120 | Electrical Rough-In | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 61 |
| L11-7116 | Frame Walls | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 60 |
| L11-7118 | Install HM Door Frame | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 63 |
| L12-7116 | Frame Walls | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 60 |
| L12-7118 | Install HM Door Frame | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 63 |

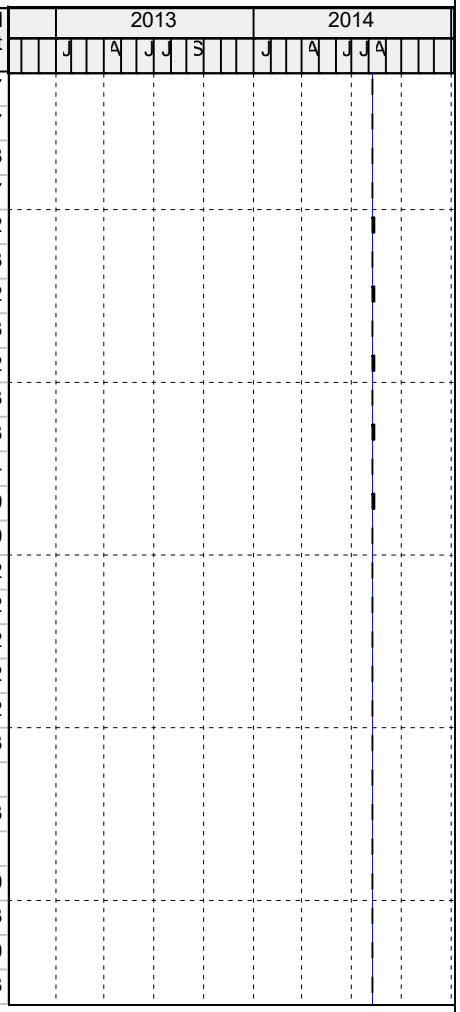



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-7116 | Frame Walls | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 60 |
| L14-7118 | Install HM Door Frame | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 63 |
| L15-7116 | Frame Walls | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 60 |
| L15-7118 | Install HM Door Frame | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 63 |
| L16-7116 | Frame Walls | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 61 |
| L16-7118 | Install HM Door Frame | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 64 |
| L17-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 58 |
| L17-7114 | HVAC Firestop & Inspect (3) | 1 | 1 | 08-Aug-14 | 08-Aug-14 | 97 |
| EL-1228 | Construct/Approve elevator lobby framing mockup (L | 3 | 3 | 08-Aug-14 | 12-Aug-14 | 13 |
| L03-8136 | Install Counter Subtops | 3 | 3 | 08-Aug-14 | 12-Aug-14 | 21 |
| MPT-1012 | Tower - Install Elevation 33 (east elevation-south end | 2 | 2 | 11-Aug-14 | 12-Aug-14 | 65 |
| L03-8606 | L3 Pool - HVAC R/I | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 56 |
| L03-7028 | GWB Hang/Tape/Finish | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 58 |
| L03-7130 | GWB Hang/Tape/Finish | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 64 |
| L04-7028 | GWB Hang/Tape/Finish | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 58 |
| L05-7026 | Inspections for GWB Cover | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 57 |
| L06-7026 | Inspections for GWB Cover | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 57 |
| L07-7026 | Inspections for GWB Cover | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 57 |
| L08-7026 | Inspections for GWB Cover | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 57 |
| L09-7028 | GWB Hang/Tape/Finish | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 58 |
| L11-7026 | Inspections for GWB Cover | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 57 |
| L04-7122 | HVAC Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 62 |
| L04-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 62 |
| L05-7122 | HVAC Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 62 |
| L05-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 62 |
| L06-7122 | HVAC Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 62 |
| L06-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 62 |

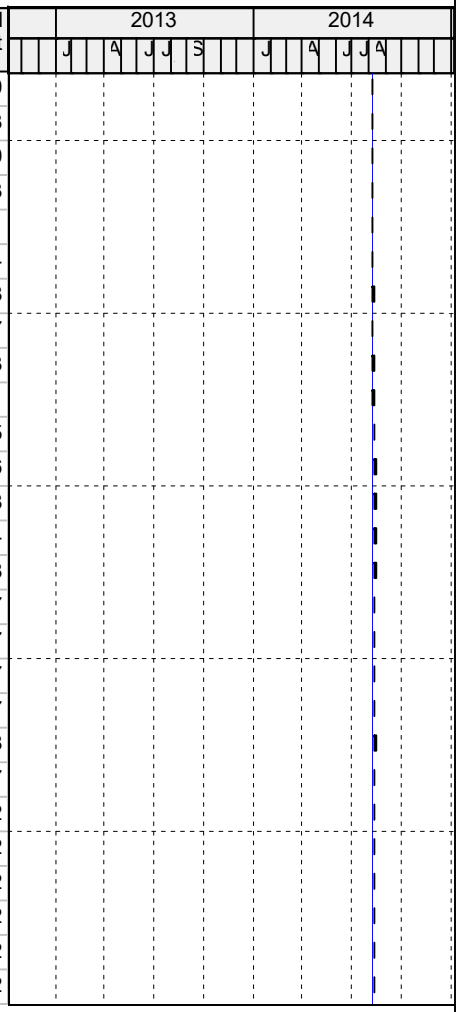



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7122 | HVAC Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 62 |
| L07-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 62 |
| L08-7122 | HVAC Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 62 |
| L08-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 62 |
| L09-7122 | HVAC Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 61 |
| L09-7124 | Fire Sprinkler Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 61 |
| L10-7122 | HVAC Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 61 |
| L10-7124 | Fire Sprinkler Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 61 |
| L11-7120 | Electrical Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 60 |
| L12-7120 | Electrical Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 60 |
| L14-7120 | Electrical Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 60 |
| L15-7120 | Electrical Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 60 |
| L16-7120 | Electrical Rough-In | 1 | 1 | 11-Aug-14 | 11-Aug-14 | 61 |
| L04-8136 | Install Counter Subtops | 3 | 3 | 11-Aug-14 | 13-Aug-14 | 23 |
| PH-6026 | PH - Insulation/Vapor Barrier/GWB at Exterior Walls | 3 | 3 | 11-Aug-14 | 13-Aug-14 | 8 |
| L02-6016a | L2 - Electrical Room Buildout | 5 | 5 | 11-Aug-14 | 15-Aug-14 | 33 |
| L11-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 22 |
| L16-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 36 |
| L11-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 23 |
| L16-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 37 |
| L05-6005 | CMU Fire Caulk/Clips | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 21 |
| L05-7028 | GWB Hang/Tape/Finish | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 57 |
| L06-7028 | GWB Hang/Tape/Finish | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 57 |
| L07-7028 | GWB Hang/Tape/Finish | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 57 |
| L08-7028 | GWB Hang/Tape/Finish | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 57 |
| L10-7026 | Inspections for GWB Cover | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 56 |
| L11-7028 | GWB Hang/Tape/Finish | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 57 |

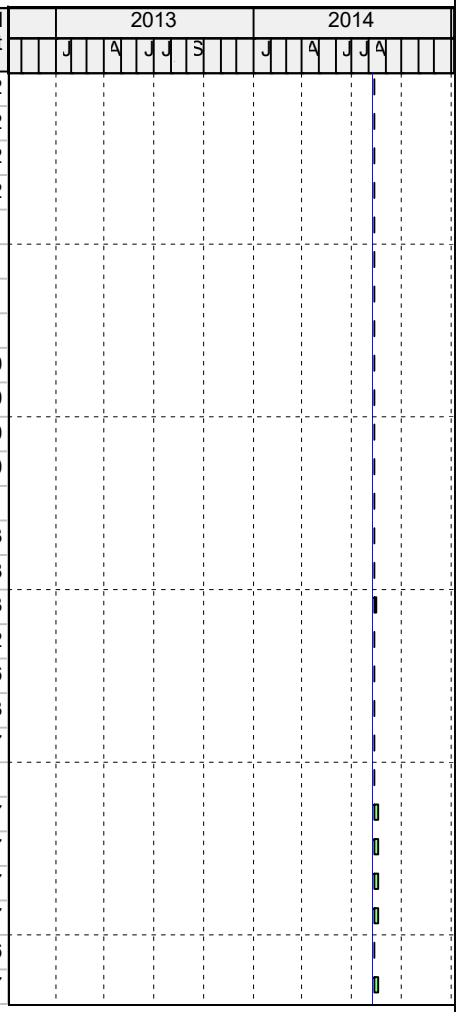



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 52 |
| L12-7016 | Install HM door frame | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 55 |
| L14-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 52 |
| L14-7016 | Install HM door frame | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 55 |
| L15-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 52 |
| L15-7016 | Install HM door frame | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 55 |
| L16-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 53 |
| L16-7016 | Install HM door frame | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 56 |
| L17-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 49 |
| L17-7008 | HVAC Firestop & Inspect (2) | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 49 |
| L04-7128 | Inspections for GWB Cover | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 62 |
| L05-7128 | Inspections for GWB Cover | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 62 |
| L06-7128 | Inspections for GWB Cover | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 62 |
| L07-7128 | Inspections for GWB Cover | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 62 |
| L08-7128 | Inspections for GWB Cover | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 62 |
| L09-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 61 |
| L10-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 61 |
| L11-7122 | HVAC Rough-In | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 60 |
| L11-7124 | Fire Sprinkler Rough-In | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 60 |
| L12-7122 | HVAC Rough-In | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 60 |
| L12-7124 | Fire Sprinkler Rough-In | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 60 |
| L14-7122 | HVAC Rough-In | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 60 |
| L14-7124 | Fire Sprinkler Rough-In | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 60 |
| L15-7122 | HVAC Rough-In | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 60 |
| L15-7124 | Fire Sprinkler Rough-In | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 60 |
| L16-7122 | HVAC Rough-In | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 61 |
| L16-7124 | Fire Sprinkler Rough-In | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 61 |

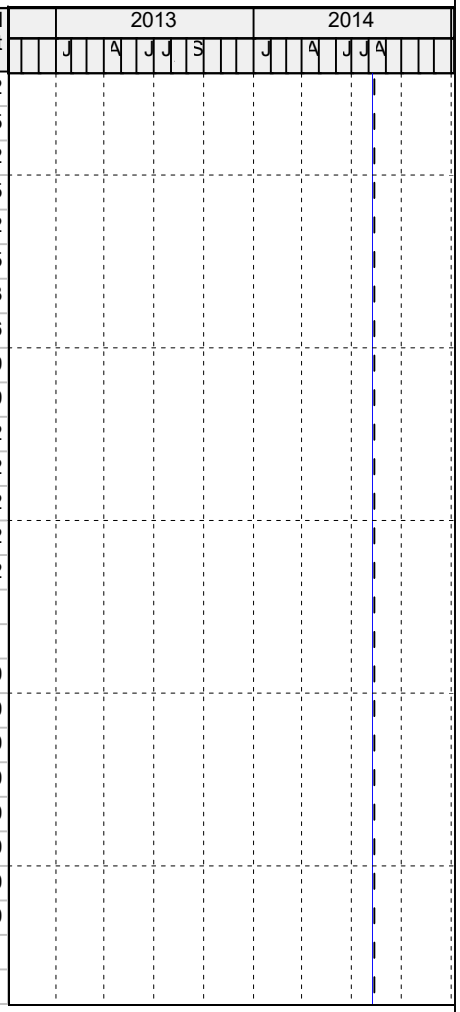



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7116 | Frame Walls | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 58 |
| L17-7118 | Install HM Door Frame | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 61 |
| L14-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 29 |
| L03-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 13-Aug-14 | 20-Aug-14 | 13 |
| L04-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 13-Aug-14 | 20-Aug-14 | 13 |
| L14-6223 | Frame Corridor Ceilings | 4 | 4 | 13-Aug-14 | 16-Aug-14 | 24 |
| L10-7028 | GWB Hang/Tape/Finish | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 56 |
| L12-7018 | Electrical Rough-In | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 52 |
| L14-7018 | Electrical Rough-In | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 52 |
| L15-7018 | Electrical Rough-In | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 52 |
| L16-7018 | Electrical Rough-In | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 53 |
| L17-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 2 | 13-Aug-14 | 14-Aug-14 | 49 |
| L17-7012 | HVAC Firestop & Inspect (3) | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 50 |
| L04-7130 | GWB Hang/Tape/Finish | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 62 |
| L05-7130 | GWB Hang/Tape/Finish | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 62 |
| L06-7130 | GWB Hang/Tape/Finish | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 62 |
| L07-7130 | GWB Hang/Tape/Finish | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 62 |
| L08-7130 | GWB Hang/Tape/Finish | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 62 |
| L09-7128 | Inspections for GWB Cover | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 61 |
| L10-7128 | Inspections for GWB Cover | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 61 |
| L11-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 60 |
| L12-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 60 |
| L14-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 60 |
| L15-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 60 |
| L16-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 61 |
| L17-7120 | Electrical Rough-In | 1 | 1 | 13-Aug-14 | 13-Aug-14 | 58 |
| L03-8138 | Install Toilet Accessories | 4 | 4 | 13-Aug-14 | 18-Aug-14 | 59 |

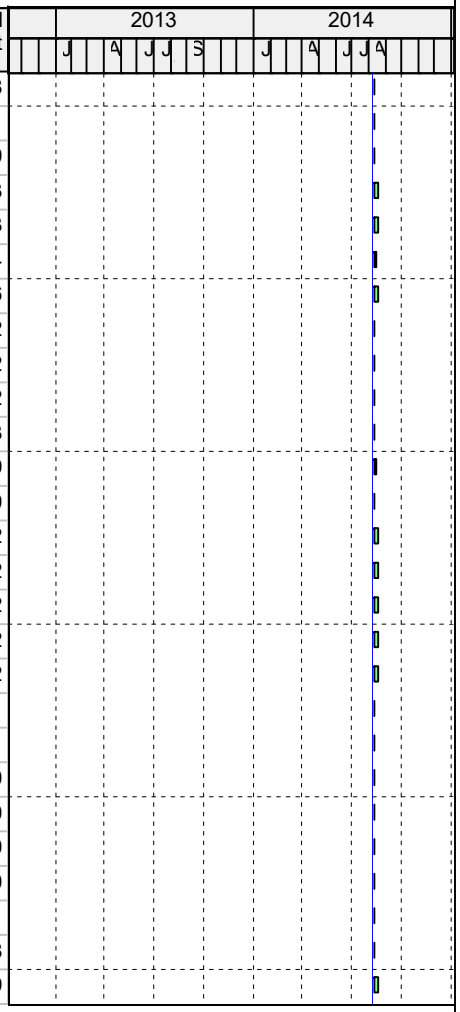



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-6005 | CMU Fire Caulk/Clips | 2 | 2 | 14-Aug-14 | 15-Aug-14 | 21 |
| L12-7020 | HVAC Rough-In | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 52 |
| L12-7022 | Fire Sprinkler Rough-In | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 52 |
| L14-7020 | HVAC Rough-In | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 52 |
| L14-7022 | Fire Sprinkler Rough-In | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 52 |
| L15-7020 | HVAC Rough-In | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 52 |
| L15-7022 | Fire Sprinkler Rough-In | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 52 |
| L16-7020 | HVAC Rough-In | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 53 |
| L16-7022 | Fire Sprinkler Rough-In | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 53 |
| L09-7130 | GWB Hang/Tape/Finish | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 61 |
| L10-7130 | GWB Hang/Tape/Finish | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 61 |
| L11-7128 | Inspections for GWB Cover | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 60 |
| L12-7128 | Inspections for GWB Cover | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 60 |
| L14-7128 | Inspections for GWB Cover | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 60 |
| L15-7128 | Inspections for GWB Cover | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 60 |
| L16-7128 | Inspections for GWB Cover | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 61 |
| L17-7122 | HVAC Rough-In | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 58 |
| L17-7124 | Fire Sprinkler Rough-In | 1 | 1 | 14-Aug-14 | 14-Aug-14 | 58 |
| L1BOH2-6008 | Int Wall Framing & Inspection | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 0 |
| LL2-2050 | LL2 - Laundry Room equipment final connections (MI | 10 | 10 | 15-Aug-14 | 28-Aug-14 | 78 |
| L12-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 15-Aug-14 | 15-Aug-14 | 52 |
| L14-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 15-Aug-14 | 15-Aug-14 | 52 |
| L15-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 15-Aug-14 | 15-Aug-14 | 52 |
| L16-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 15-Aug-14 | 15-Aug-14 | 53 |
| L17-7014 | Frame Wall & Soffit (x41/x42) | 1 | 1 | 15-Aug-14 | 15-Aug-14 | 49 |
| L17-7016 | Install HM door frame | 1 | 1 | 15-Aug-14 | 15-Aug-14 | 52 |
| L11-7130 | GWB Hang/Tape/Finish | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 60 |

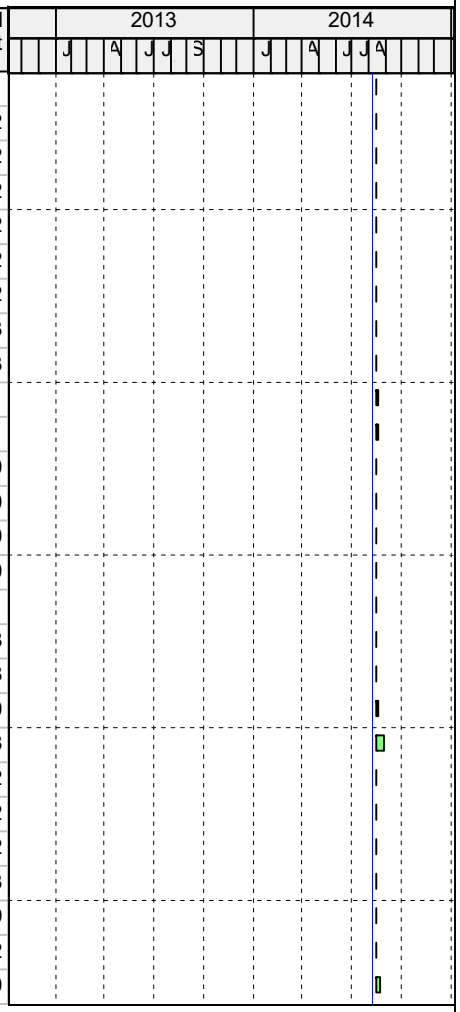



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7130 | GWB Hang/Tape/Finish | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 60 |
| L14-7130 | GWB Hang/Tape/Finish | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 60 |
| L15-7130 | GWB Hang/Tape/Finish | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 60 |
| L16-7130 | GWB Hang/Tape/Finish | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 61 |
| L17-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 15-Aug-14 | 15-Aug-14 | 58 |
| L04-8138 | Install Toilet Accessories | 4 | 4 | 15-Aug-14 | 19-Aug-14 | 71 |
| L05-8136 | Install Counter Subtops | 3 | 3 | 15-Aug-14 | 19-Aug-14 | 23 |
| LL2-8106a | LL2 - Pinned Insulation @ Ramp Ceiling | 3 | 3 | 15-Aug-14 | 19-Aug-14 | 33 |
| LL1-6014Ia | L1 bar redesign - rework plumbing at ceilings | 10 | 10 | 18-Aug-14 | 29-Aug-14 | 30 |
| L02-5102 | L2 - Storefront Frames | 3 | 3 | 18-Aug-14* | 20-Aug-14 | 0 |
| L07-6005 | CMU Fire Caulk/Clips | 2 | 2 | 18-Aug-14 | 19-Aug-14 | 21 |
| L15-6223 | Frame Corridor Ceilings | 4 | 4 | 18-Aug-14 | 21-Aug-14 | 20 |
| L03-8201 | Install ACT Grid @ Corridors | 2 | 2 | 18-Aug-14* | 19-Aug-14 | 54 |
| L04-8201 | Install ACT Grid @ Corridors | 2 | 2 | 18-Aug-14 | 19-Aug-14 | 54 |
| L03-7030 | Paint | 1 | 1 | 18-Aug-14 | 18-Aug-14 | 58 |
| L03-7132 | Paint | 1 | 1 | 18-Aug-14 | 18-Aug-14 | 64 |
| L04-7030 | Paint | 1 | 1 | 18-Aug-14 | 18-Aug-14 | 58 |
| L09-7030 | Paint | 1 | 1 | 18-Aug-14 | 18-Aug-14 | 58 |
| L12-7026 | Inspections for GWB Cover | 1 | 1 | 18-Aug-14 | 18-Aug-14 | 52 |
| L14-7026 | Inspections for GWB Cover | 1 | 1 | 18-Aug-14 | 18-Aug-14 | 52 |
| L15-7026 | Inspections for GWB Cover | 1 | 1 | 18-Aug-14 | 18-Aug-14 | 52 |
| L16-7026 | Inspections for GWB Cover | 1 | 1 | 18-Aug-14 | 18-Aug-14 | 53 |
| L17-7018 | Electrical Rough-In | 1 | 1 | 18-Aug-14 | 18-Aug-14 | 49 |
| L17-7128 | Inspections for GWB Cover | 1 | 1 | 18-Aug-14 | 18-Aug-14 | 58 |
| L05-8138 | Install Toilet Accessories | 3 | 3 | 18-Aug-14 | 20-Aug-14 | 62 |
| L06-8138 | Install Toilet Accessories | 4 | 4 | 18-Aug-14 | 21-Aug-14 | 60 |
| LL1-6014Ic | L1 bar redesign - rework electrical at ceilings | 10 | 10 | 18-Aug-14 | 29-Aug-14 | 30 |

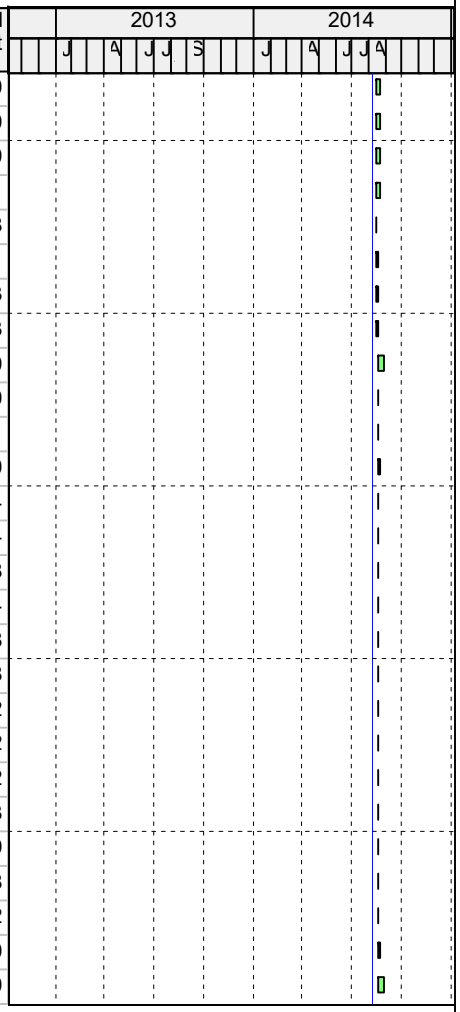



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| RF-4008 | Tower Roof - Coping / Flashing | 10 | 10 | 19-Aug-14 | 02-Sep-14 | 81 |
| I-4004 | East Stitched - Install metal panels | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 81 |
| L05-8201 | Install ACT Grid @ Corridors | 2 | 2 | 19-Aug-14 | 20-Aug-14 | 54 |
| L03-7032 | Install VCT Flooring (x42) | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 58 |
| L03-7134 | Install VCT Flooring | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 64 |
| L04-7032 | Install VCT Flooring (x42) | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 58 |
| L05-7030 | Paint | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 57 |
| L06-7030 | Paint | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 57 |
| L07-7030 | Paint | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 57 |
| L08-7030 | Paint | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 57 |
| L09-7032 | Install VCT Flooring (x42) | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 58 |
| L11-7030 | Paint | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 57 |
| L12-7028 | GWB Hang/Tape/Finish | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 52 |
| L14-7028 | GWB Hang/Tape/Finish | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 52 |
| L15-7028 | GWB Hang/Tape/Finish | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 52 |
| L16-7028 | GWB Hang/Tape/Finish | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 53 |
| L17-7020 | HVAC Rough-In | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 49 |
| L17-7022 | Fire Sprinkler Rough-In | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 49 |
| L17-7130 | GWB Hang/Tape/Finish | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 58 |
| MPT-1014 | Tower - Install Elevations 46-49 (north elevation-roof) | 8 | 8 | 19-Aug-14 | 28-Aug-14 | 61 |
| L08-6005 | CMU Fire Caulk/Clips | 2 | 2 | 20-Aug-14 | 21-Aug-14 | 21 |
| L03-7034 | Install Door and Hardware (x42) | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 58 |
| L03-7136 | Install Door and Hardware | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 64 |
| L04-7034 | Install Door and Hardware (x42) | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 58 |
| L05-7032 | Install VCT Flooring (x42) | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 57 |
| L06-7032 | Install VCT Flooring (x42) | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 57 |
| L07-7032 | Install VCT Flooring (x42) | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 57 |

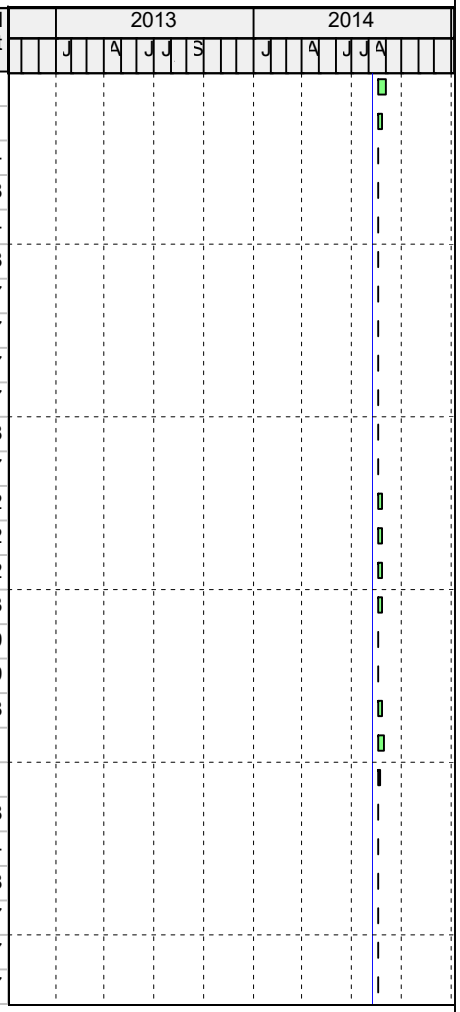



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7032 | Install VCT Flooring (x42) | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 57 |
| L09-7034 | Install Door and Hardware (x42) | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 58 |
| L10-7030 | Paint | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 56 |
| L11-7032 | Install VCT Flooring (x42) | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 57 |
| L17-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 49 |
| L04-7132 | Paint | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 62 |
| L05-7132 | Paint | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 62 |
| L06-7132 | Paint | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 62 |
| L07-7132 | Paint | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 62 |
| L08-7132 | Paint | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 62 |
| L06-8136 | Install Counter Subtops | 3 | 3 | 20-Aug-14 | 22-Aug-14 | 23 |
| L03-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 40 |
| L04-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 40 |
| L05-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 21-Aug-14 | 28-Aug-14 | 13 |
| L06-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 21-Aug-14 | 28-Aug-14 | 13 |
| L02-5104 | L2 - Storefront Glazing | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 0 |
| L03-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 21-Aug-14 | 25-Aug-14 | 58 |
| L03-7138 | Electrical Trim-Out | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 64 |
| L04-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 21-Aug-14 | 25-Aug-14 | 58 |
| L05-7034 | Install Door and Hardware (x42) | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 57 |
| L06-7034 | Install Door and Hardware (x42) | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 57 |
| L07-7034 | Install Door and Hardware (x42) | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 57 |
| L08-7034 | Install Door and Hardware (x42) | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 57 |
| L09-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 21-Aug-14 | 25-Aug-14 | 58 |
| L10-7032 | Install VCT Flooring (x42) | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 56 |
| L11-7034 | Install Door and Hardware (x42) | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 57 |
| L17-7026 | Inspections for GWB Cover | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 49 |

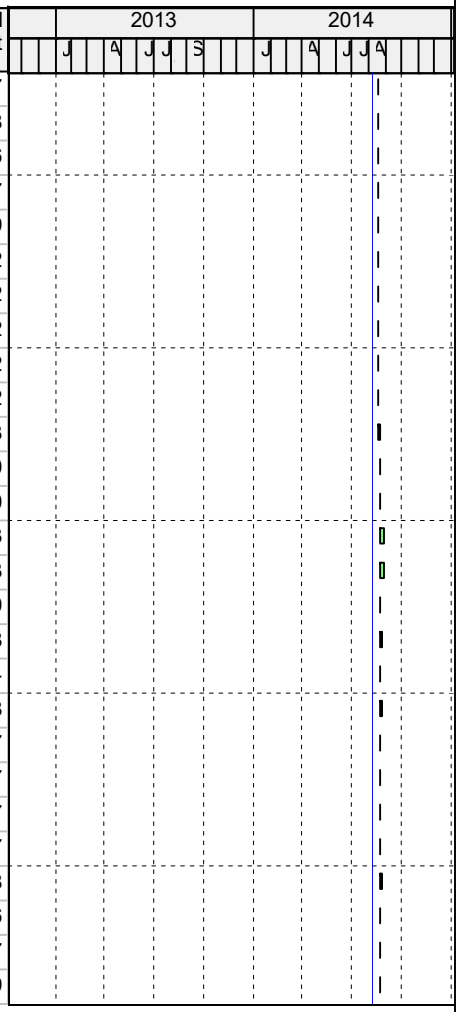



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7134 | Install VCT Flooring | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 62 |
| L05-7134 | Install VCT Flooring | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 62 |
| L06-7134 | Install VCT Flooring | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 62 |
| L07-7134 | Install VCT Flooring | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 62 |
| L08-7134 | Install VCT Flooring | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 62 |
| L09-7132 | Paint | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 61 |
| L10-7132 | Paint | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 61 |
| L03-8634 | Pool - Install reinforcing steel & inspect | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 13 |
| L1BOH2-6016 | Electrical RI | 4 | 4 | 21-Aug-14 | 26-Aug-14 | 21 |
| L1BOH2-6022 | Fire Alarm / Elec Specialties RI | 4 | 4 | 21-Aug-14 | 26-Aug-14 | 21 |
| L1BOH2-6018 | HVAC RI | 4 | 4 | 21-Aug-14 | 26-Aug-14 | 21 |
| L03-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 41 |
| L04-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 41 |
| L03-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 41 |
| L04-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 41 |
| L09-6005 | CMU Fire Caulk/Clips | 2 | 2 | 22-Aug-14 | 25-Aug-14 | 21 |
| L16-6223 | Frame Corridor Ceilings | 4 | 4 | 22-Aug-14 | 26-Aug-14 | 25 |
| L06-8201 | Install ACT Grid @ Corridors | 2 | 2 | 22-Aug-14 | 25-Aug-14 | 54 |
| L05-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 22-Aug-14 | 26-Aug-14 | 57 |
| L06-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 22-Aug-14 | 26-Aug-14 | 57 |
| L07-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 22-Aug-14 | 26-Aug-14 | 57 |
| L08-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 22-Aug-14 | 26-Aug-14 | 57 |
| L10-7034 | Install Door and Hardware (x42) | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 56 |
| L11-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 22-Aug-14 | 26-Aug-14 | 57 |
| L17-7028 | GWB Hang/Tape/Finish | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 49 |
| L04-7136 | Install Door and Hardware | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 62 |
| L05-7136 | Install Door and Hardware | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 62 |

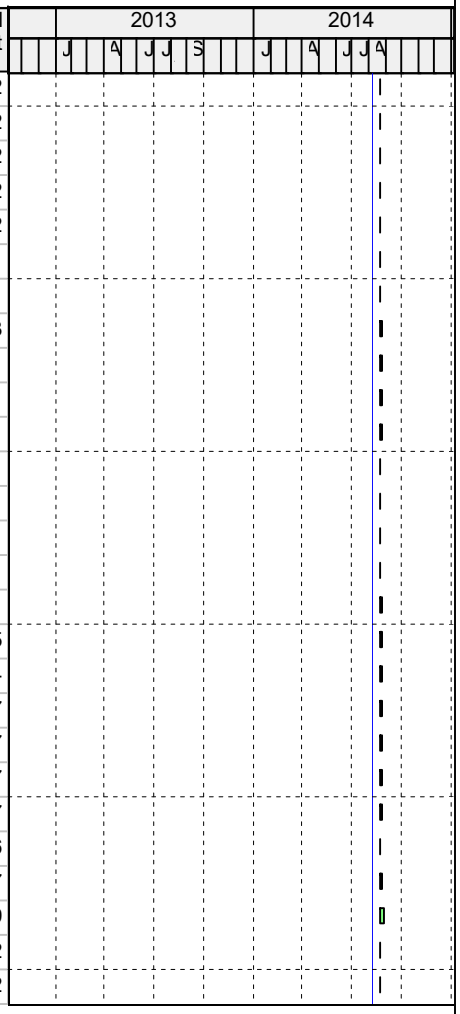



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7136 | Install Door and Hardware | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 62 |
| L07-7136 | Install Door and Hardware | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 62 |
| L08-7136 | Install Door and Hardware | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 62 |
| L09-7134 | Install VCT Flooring | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 61 |
| L10-7134 | Install VCT Flooring | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 61 |
| L11-7132 | Paint | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 60 |
| L12-7132 | Paint | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 60 |
| L14-7132 | Paint | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 60 |
| L15-7132 | Paint | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 60 |
| L16-7132 | Paint | 1 | 1 | 22-Aug-14 | 22-Aug-14 | 61 |
| LL1-8102a | GWB Hang/Tape (Ceilings) | 18 | 18 | 22-Aug-14 | 17-Sep-14 | 30 |
| L03-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 41 |
| L04-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 41 |
| L03-8405 | Cover Inspection | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 41 |
| L04-8405 | Cover Inspection | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 41 |
| L03-8129 | Install Shower Doors | 4 | 4 | 25-Aug-14 | 28-Aug-14 | 35 |
| L04-8129 | Install Shower Doors | 4 | 4 | 25-Aug-14 | 28-Aug-14 | 35 |
| L03-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 25-Aug-14 | 29-Aug-14 | 64 |
| L10-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 25-Aug-14 | 27-Aug-14 | 56 |
| L04-7138 | Electrical Trim-Out | 2 | 2 | 25-Aug-14 | 26-Aug-14 | 62 |
| L05-7138 | Electrical Trim-Out | 2 | 2 | 25-Aug-14 | 26-Aug-14 | 62 |
| L06-7138 | Electrical Trim-Out | 2 | 2 | 25-Aug-14 | 26-Aug-14 | 62 |
| L07-7138 | Electrical Trim-Out | 2 | 2 | 25-Aug-14 | 26-Aug-14 | 62 |
| L08-7138 | Electrical Trim-Out | 2 | 2 | 25-Aug-14 | 26-Aug-14 | 62 |
| L09-7136 | Install Door and Hardware | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 61 |
| L10-7136 | Install Door and Hardware | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 61 |
| L11-7134 | Install VCT Flooring | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 60 |

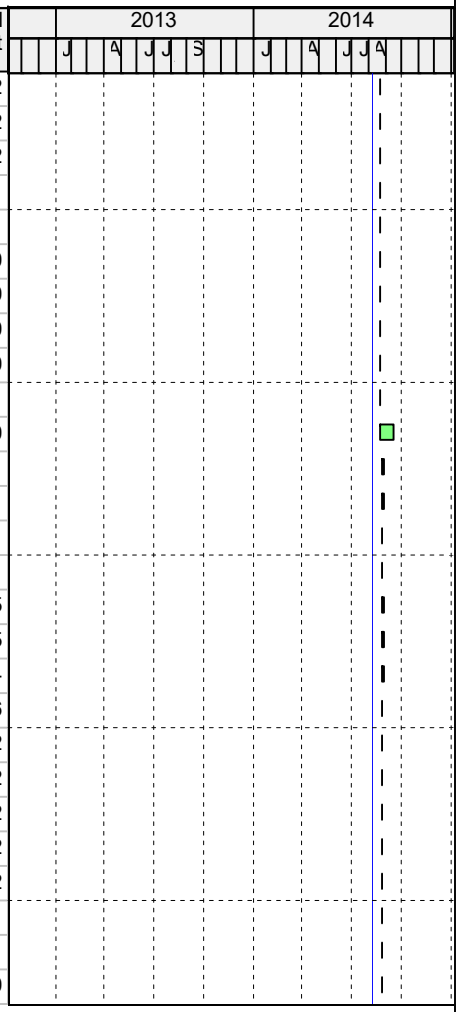



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7134 | Install VCT Flooring | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 60 |
| L14-7134 | Install VCT Flooring | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 60 |
| L15-7134 | Install VCT Flooring | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 60 |
| L16-7134 | Install VCT Flooring | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 61 |
| L07-8138 | Install Toilet Accessories | 4 | 4 | 25-Aug-14 | 28-Aug-14 | 23 |
| L03-8140 | Counterops On Site | 0 | 0 | 25-Aug-14* | | 14 |
| L03-8129a | Shower Doors On Site | 0 | 0 | 25-Aug-14* | | 35 |
| L10-6005 | CMU Fire Caulk/Clips | 2 | 2 | 26-Aug-14 | 27-Aug-14 | 21 |
| L03-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 30 |
| L04-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 30 |
| L07-8201 | Install ACT Grid @ Corridors | 2 | 2 | 26-Aug-14 | 27-Aug-14 | 54 |
| L03-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 26-Aug-14 | 27-Aug-14 | 58 |
| L04-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 26-Aug-14 | 27-Aug-14 | 58 |
| L09-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 26-Aug-14 | 27-Aug-14 | 58 |
| L12-7030 | Paint | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 52 |
| L14-7030 | Paint | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 52 |
| L15-7030 | Paint | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 52 |
| L16-7030 | Paint | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 53 |
| L09-7138 | Electrical Trim-Out | 2 | 2 | 26-Aug-14 | 27-Aug-14 | 61 |
| L10-7138 | Electrical Trim-Out | 2 | 2 | 26-Aug-14 | 27-Aug-14 | 61 |
| L11-7136 | Install Door and Hardware | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 60 |
| L12-7136 | Install Door and Hardware | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 60 |
| L14-7136 | Install Door and Hardware | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 60 |
| L15-7136 | Install Door and Hardware | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 60 |
| L16-7136 | Install Door and Hardware | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 61 |
| L17-7132 | Paint | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 58 |
| L03-8124d | Flooring On Site and Acclimated | 2 | 2 | 26-Aug-14* | 27-Aug-14 | 20 |

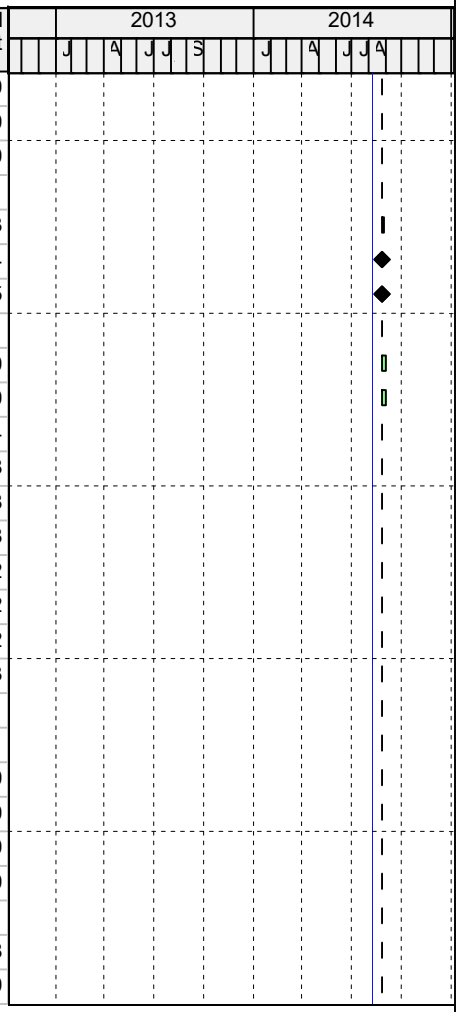



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8123 | Bathroom "Barn Doors" On Site | 0 | 0 | 26-Aug-14* | | 30 |
| L17-6223 | Frame Corridor Ceilings | 4 | 4 | 27-Aug-14 | 02-Sep-14 | 21 |
| L05-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 57 |
| L06-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 57 |
| L07-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 57 |
| L08-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 57 |
| L11-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 57 |
| L12-7032 | Install VCT Flooring (x42) | 1 | 1 | 27-Aug-14 | 27-Aug-14 | 52 |
| L14-7032 | Install VCT Flooring (x42) | 1 | 1 | 27-Aug-14 | 27-Aug-14 | 52 |
| L15-7032 | Install VCT Flooring (x42) | 1 | 1 | 27-Aug-14 | 27-Aug-14 | 52 |
| L16-7032 | Install VCT Flooring (x42) | 1 | 1 | 27-Aug-14 | 27-Aug-14 | 53 |
| L04-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 62 |
| L05-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 62 |
| L06-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 62 |
| L07-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 62 |
| L08-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 62 |
| L11-7138 | Electrical Trim-Out | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 60 |
| L12-7138 | Electrical Trim-Out | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 60 |
| L14-7138 | Electrical Trim-Out | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 60 |
| L15-7138 | Electrical Trim-Out | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 60 |
| L16-7138 | Electrical Trim-Out | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 61 |
| L17-7134 | Install VCT Flooring | 1 | 1 | 27-Aug-14 | 27-Aug-14 | 58 |
| L07-8136 | Install Counter Subtops | 3 | 3 | 27-Aug-14 | 29-Aug-14 | 22 |
| L1BOH2-8130 | Inspections For Cover | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 21 |
| L11-6005 | CMU Fire Caulk/Clips | 2 | 2 | 28-Aug-14 | 29-Aug-14 | 21 |
| L05-8129 | Install Shower Doors | 4 | 4 | 28-Aug-14 | 03-Sep-14 | 35 |
| L06-8129 | Install Shower Doors | 4 | 4 | 28-Aug-14 | 03-Sep-14 | 35 |

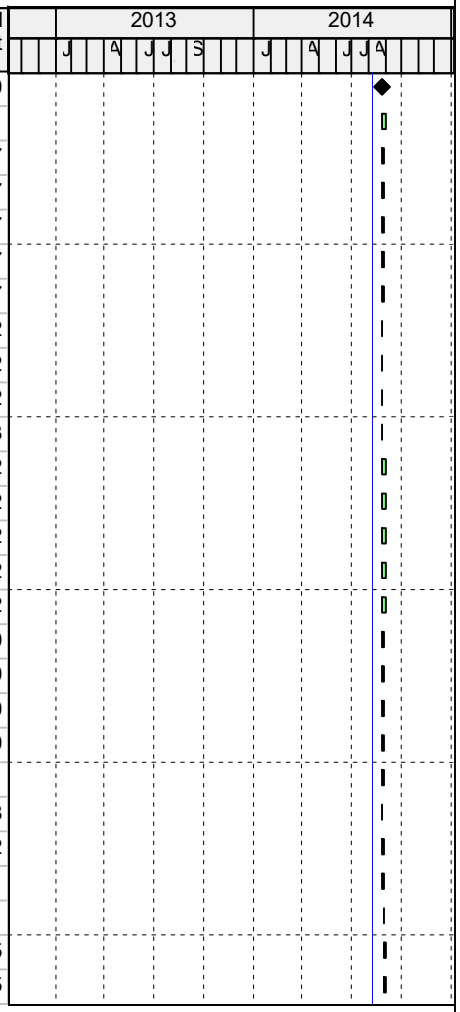



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8201 | Install ACT Grid @ Corridors | 2 | 2 | 28-Aug-14 | 29-Aug-14 | 54 |
| L03-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 58 |
| L04-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 58 |
| L09-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 58 |
| L10-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 28-Aug-14 | 29-Aug-14 | 56 |
| L12-7034 | Install Door and Hardware (x42) | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 52 |
| L14-7034 | Install Door and Hardware (x42) | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 52 |
| L15-7034 | Install Door and Hardware (x42) | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 52 |
| L16-7034 | Install Door and Hardware (x42) | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 53 |
| L09-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 61 |
| L10-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 61 |
| L17-7136 | Install Door and Hardware | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 58 |
| L03-8636 | Pool - Shotcrete | 1 | 1 | 28-Aug-14 | 28-Aug-14 | 13 |
| L08-8136 | Install Counter Subtops | 3 | 3 | 28-Aug-14 | 02-Sep-14 | 25 |
| L1BOH2-8100 | Insulation | 4 | 4 | 29-Aug-14 | 04-Sep-14 | 21 |
| L03-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 29-Aug-14 | 29-Aug-14 | 41 |
| L05-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 29-Aug-14 | 29-Aug-14 | 35 |
| L06-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 29-Aug-14 | 29-Aug-14 | 55 |
| L04-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 29-Aug-14 | 29-Aug-14 | 41 |
| L07-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 29-Aug-14 | 08-Sep-14 | 13 |
| L08-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 29-Aug-14 | 08-Sep-14 | 13 |
| L09-8201 | Install ACT Grid @ Corridors | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 54 |
| L05-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 57 |
| L06-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 57 |
| L07-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 57 |
| L08-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 57 |
| L11-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 57 |

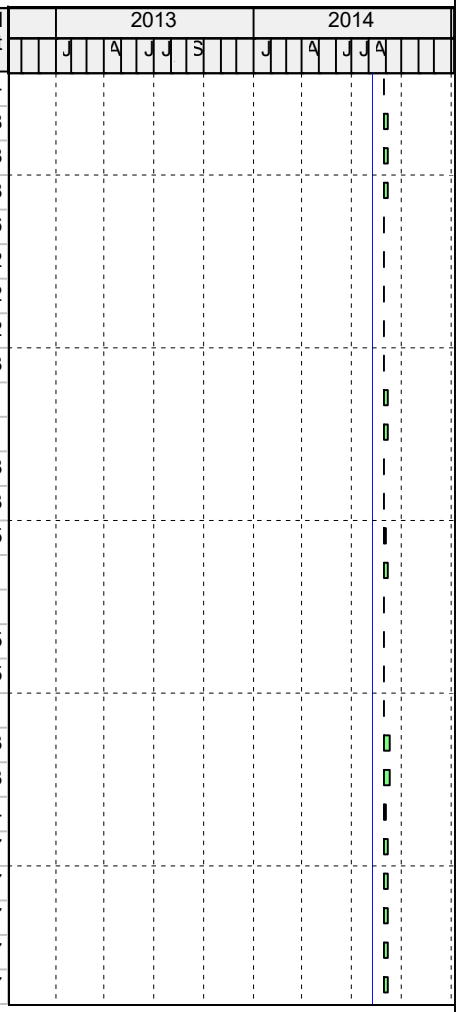



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 29-Aug-14 | 03-Sep-14 | 52 |
| L14-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 29-Aug-14 | 03-Sep-14 | 52 |
| L15-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 29-Aug-14 | 03-Sep-14 | 52 |
| L16-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 29-Aug-14 | 03-Sep-14 | 53 |
| L17-7030 | Paint | 1 | 1 | 29-Aug-14 | 29-Aug-14 | 49 |
| L11-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 60 |
| L12-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 60 |
| L14-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 60 |
| L15-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 60 |
| L16-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 61 |
| L17-7138 | Electrical Trim-Out | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 58 |
| L08-8138 | Install Toilet Accessories | 4 | 4 | 29-Aug-14 | 04-Sep-14 | 23 |
| L03-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 02-Sep-14 | 02-Sep-14 | 41 |
| L04-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 02-Sep-14 | 02-Sep-14 | 41 |
| L05-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 02-Sep-14 | 02-Sep-14 | 35 |
| L06-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 02-Sep-14 | 02-Sep-14 | 56 |
| LL1-6014lb | L1 bar redesign - rework ceiling framing | 5 | 5 | 02-Sep-14 | 08-Sep-14 | 30 |
| L05-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 02-Sep-14 | 02-Sep-14 | 35 |
| L06-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 02-Sep-14 | 02-Sep-14 | 56 |
| MPL4-1000 | Upper L4 Ballroom - Install Elevations 1, 2 & 3 (south | 4 | 4 | 02-Sep-14 | 05-Sep-14 | 61 |
| MPL4-1002 | Upper L4 Ballroom - Install Elevation 10 (west elevati | 4 | 4 | 02-Sep-14 | 05-Sep-14 | 73 |
| MPL4-1004 | Upper L4 Ballroom - Install Elevation 9 (north elevatio | 4 | 4 | 02-Sep-14 | 05-Sep-14 | 73 |
| L12-6005 | CMU Fire Caulk/Clips | 2 | 2 | 02-Sep-14 | 03-Sep-14 | 21 |
| L05-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 02-Sep-14 | 06-Sep-14 | 36 |
| L06-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 02-Sep-14 | 06-Sep-14 | 36 |
| L10-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 02-Sep-14 | 08-Sep-14 | 56 |
| L17-7032 | Install VCT Flooring (x42) | 1 | 1 | 02-Sep-14 | 02-Sep-14 | 49 |

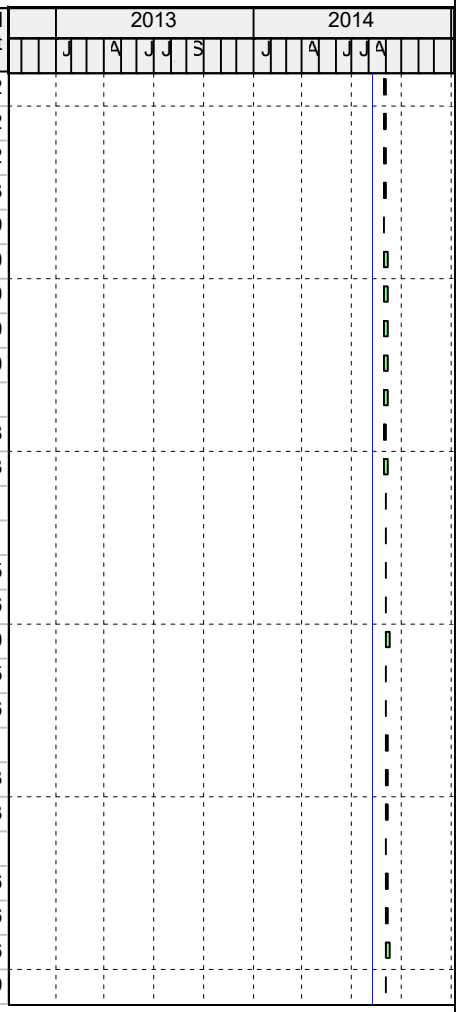


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPT-1016 | Tower - Install Elevations 29-31 (south end-roof) | 6 | 6 | 02-Sep-14 | 09-Sep-14 | 71 |
| MPT-1018 | Tower - Install Elevations 36b, 37-39 (roof penthouse | 8 | 8 | 02-Sep-14 | 11-Sep-14 | 69 |
| MPT-1020 | Tower - Install Elevations 41 & 44 (east elevation-nort | 3 | 3 | 02-Sep-14 | 04-Sep-14 | 74 |
| LL1-Z2-8102a | GWB Hang (Ceilings) & Inspection | 9 | 9 | 02-Sep-14 | 12-Sep-14 | 24 |
| L17-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 03-Sep-14 | 04-Sep-14 | 24 |
| L17-6040 | Test Heat Pumps - L15, L16 and L17 | 3 | 3 | 03-Sep-14 | 05-Sep-14 | 22 |
| L17-6036 | Framing Around Heat Pump & Soffit | 3 | 3 | 03-Sep-14 | 05-Sep-14 | 22 |
| L03-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 03-Sep-14 | 04-Sep-14 | 41 |
| L04-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 03-Sep-14 | 04-Sep-14 | 41 |
| L05-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 35 |
| L06-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 56 |
| LL2E-8340 | LL2 - Install walk-in cooler/freezer (BY OTHERS) | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 29 |
| L05-8405 | Cover Inspection | 1 | 1 | 03-Sep-14 | 03-Sep-14 | 35 |
| L06-8405 | Cover Inspection | 1 | 1 | 03-Sep-14 | 03-Sep-14 | 56 |
| MPP-1008 | Podium - Install Elevations 7 & 8 (north & east elevati | 9 | 9 | 03-Sep-14 | 15-Sep-14 | 61 |
| MPP-1010 | Podium - Install Elevations 5 & 6 (east elevation, sou | 4 | 4 | 03-Sep-14 | 08-Sep-14 | 61 |
| L17-7034 | Install Door and Hardware (x42) | 1 | 1 | 03-Sep-14 | 03-Sep-14 | 49 |
| L17-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 58 |
| L09-8136 | Install Counter Subtops | 3 | 3 | 03-Sep-14 | 05-Sep-14 | 26 |
| L10-8136 | Install Counter Subtops | 3 | 3 | 03-Sep-14 | 05-Sep-14 | 46 |
| L14-6005 | CMU Fire Caulk/Clips | 2 | 2 | 04-Sep-14 | 05-Sep-14 | 21 |
| L07-8129 | Install Shower Doors | 4 | 4 | 04-Sep-14 | 09-Sep-14 | 35 |
| L08-8129 | Install Shower Doors | 4 | 4 | 04-Sep-14 | 09-Sep-14 | 35 |
| L10-8201 | Install ACT Grid @ Corridors | 2 | 2 | 04-Sep-14 | 05-Sep-14 | 54 |
| L12-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 04-Sep-14 | 05-Sep-14 | 52 |
| L14-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 04-Sep-14 | 05-Sep-14 | 52 |
| L15-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 04-Sep-14 | 05-Sep-14 | 52 |

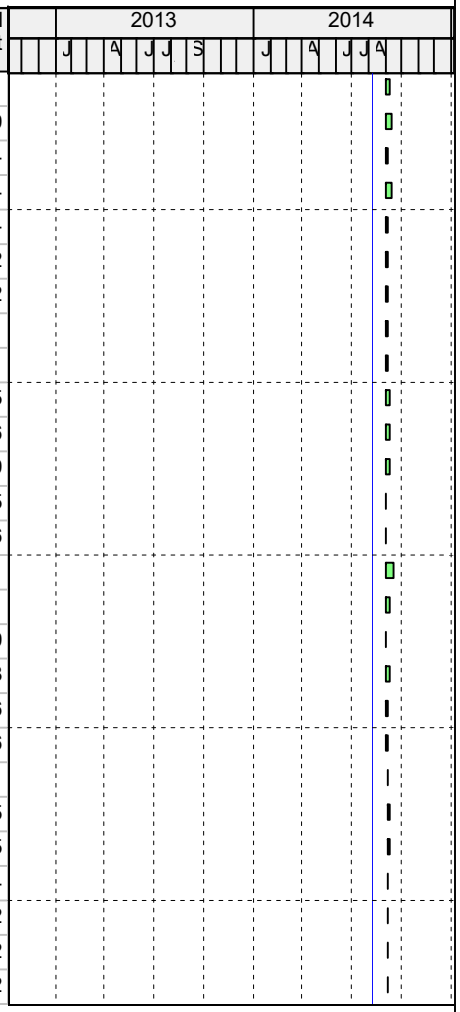



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 04-Sep-14 | 05-Sep-14 | 53 |
| L17-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 04-Sep-14 | 08-Sep-14 | 49 |
| L1BOH2-8102 | GWB Hang (Walls) | 4 | 4 | 05-Sep-14 | 10-Sep-14 | 21 |
| L03-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 05-Sep-14 | 05-Sep-14 | 41 |
| L04-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 05-Sep-14 | 05-Sep-14 | 41 |
| L03-7042 | Install Tile Flooring (x41) | 2 | 2 | 05-Sep-14 | 08-Sep-14 | 58 |
| L04-7042 | Install Tile Flooring (x41) | 2 | 2 | 05-Sep-14 | 08-Sep-14 | 58 |
| L09-7042 | Install Tile Flooring (x41) | 2 | 2 | 05-Sep-14 | 08-Sep-14 | 58 |
| L09-8138 | Install Toilet Accessories | 4 | 4 | 05-Sep-14 | 10-Sep-14 | 23 |
| L17-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 22 |
| L03-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 41 |
| L03-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 41 |
| L04-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 41 |
| L04-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 41 |
| L15-6005 | CMU Fire Caulk/Clips | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 21 |
| L07-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 30 |
| L08-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 30 |
| L05-7042 | Install Tile Flooring (x41) | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 57 |
| L06-7042 | Install Tile Flooring (x41) | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 57 |
| L07-7042 | Install Tile Flooring (x41) | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 57 |
| L08-7042 | Install Tile Flooring (x41) | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 57 |
| L11-7042 | Install Tile Flooring (x41) | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 57 |
| L12-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 52 |
| L14-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 52 |
| L15-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 52 |
| L16-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 53 |
| L03-8418 | Flooring at Elevator Lobby | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 62 |

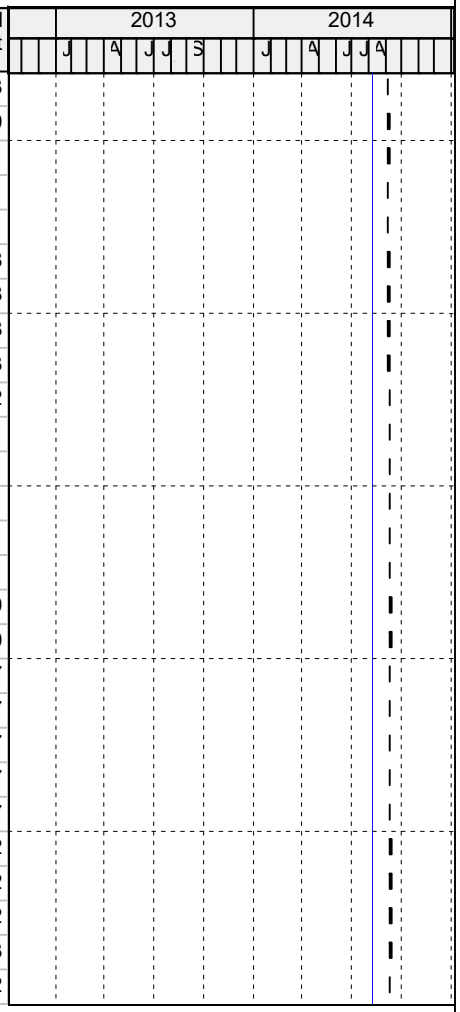



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 50 |
| L08-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 49 |
| L04-8418 | Flooring at Elevator Lobby | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 62 |
| L05-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 35 |
| L06-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 56 |
| L09-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 09-Sep-14 | 16-Sep-14 | 13 |
| L10-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 09-Sep-14 | 16-Sep-14 | 13 |
| L03-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 58 |
| L04-7044 | Install Vending Cabinets (x41) | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 58 |
| L09-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 58 |
| L10-7042 | Install Tile Flooring (x41) | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 56 |
| L17-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 49 |
| L11-8136 | Install Counter Subtops | 3 | 3 | 09-Sep-14 | 11-Sep-14 | 44 |
| LL1-6014lb2 | L1 bar redesign - GWB hang at ceilings | 4 | 4 | 09-Sep-14 | 12-Sep-14 | 30 |
| L05-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 35 |
| L06-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 56 |
| L07-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 50 |
| L08-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 50 |
| LL2E-8342 | LL2 - Final connections at walk-in cooler/freezer | 5 | 5 | 10-Sep-14 | 16-Sep-14 | 60 |
| L07-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 50 |
| L08-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 50 |
| MPP-1000 | Podium - Install Elevations 3 & 4 (south elevation) | 4 | 4 | 10-Sep-14 | 15-Sep-14 | 61 |
| L16-6005 | CMU Fire Caulk/Clips | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 21 |
| L09-8129 | Install Shower Doors | 4 | 4 | 10-Sep-14 | 13-Sep-14 | 42 |
| L10-8129 | Install Shower Doors | 4 | 4 | 10-Sep-14 | 13-Sep-14 | 42 |
| L11-8201 | Install ACT Grid @ Corridors | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 29 |
| L05-7044 | Install Vending Cabinets (x41) | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 57 |

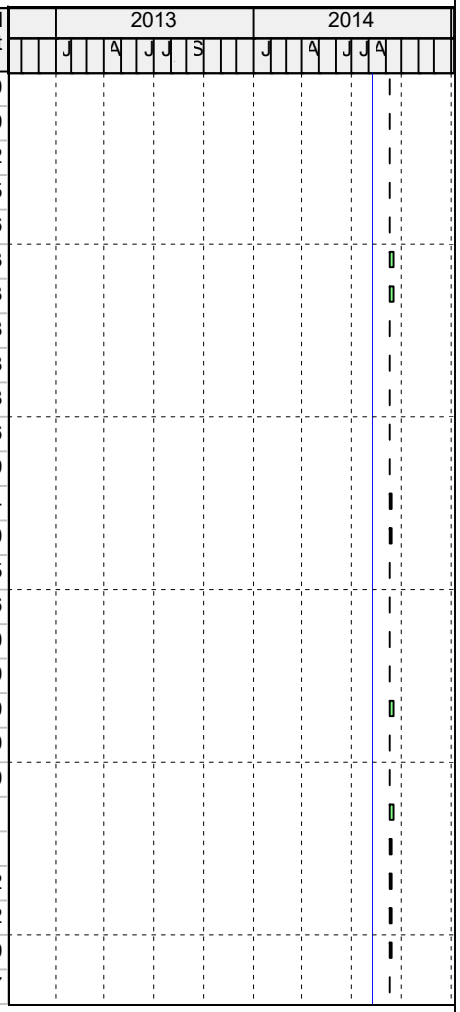



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7044 | Install Vending Cabinets (x41) | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 57 |
| L07-7044 | Install Vending Cabinets (x41) | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 57 |
| L08-7044 | Install Vending Cabinets (x41) | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 57 |
| L11-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 57 |
| L03-8126a | Doors & Hardware On Site | 0 | 0 | 10-Sep-14* | | 21 |
| L1BOH2-8215 | GWB Tape (Walls) | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 21 |
| L05-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 35 |
| L06-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 56 |
| L07-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 50 |
| L08-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 50 |
| L07-8405 | Cover Inspection | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 50 |
| L08-8405 | Cover Inspection | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 50 |
| L10-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 56 |
| L17-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 49 |
| L10-8138 | Install Toilet Accessories | 4 | 4 | 11-Sep-14 | 16-Sep-14 | 23 |
| L1K-8102a | GWB Hang (Ceilings at Public Restroom) & Inspectio | 4 | 4 | 11-Sep-14 | 16-Sep-14 | 20 |
| L05-8206a | Install Base @ Corridors | 3 | 3 | 11-Sep-14 | 15-Sep-14 | 54 |
| L17-6005 | CMU Fire Caulk/Clips | 2 | 2 | 12-Sep-14 | 15-Sep-14 | 28 |
| L05-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 35 |
| L06-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 56 |
| L09-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 30 |
| L10-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 30 |
| L11-8129 | Install Shower Doors | 4 | 4 | 15-Sep-14 | 18-Sep-14 | 35 |
| L12-8129 | Install Shower Doors | 4 | 4 | 15-Sep-14 | 18-Sep-14 | 35 |
| L12-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 30 |
| L12-7042 | Install Tile Flooring (x41) | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 52 |
| L14-7042 | Install Tile Flooring (x41) | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 52 |

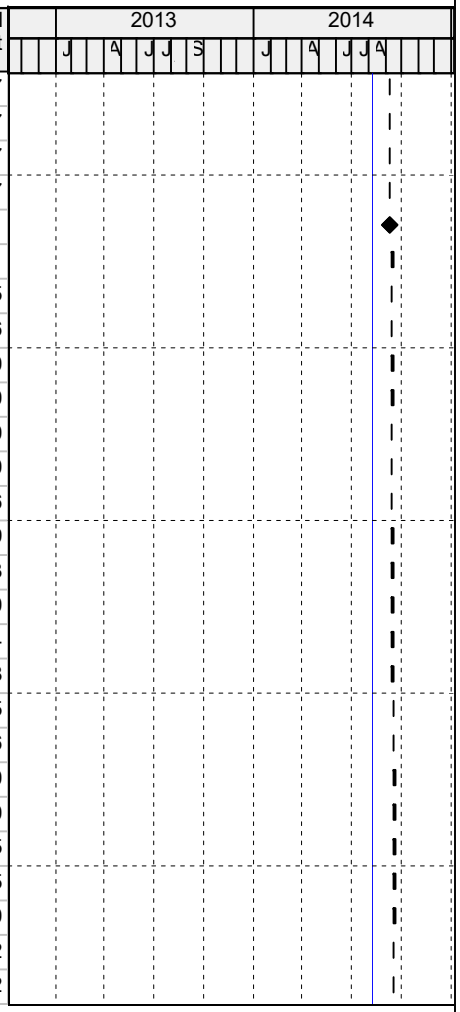



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-7042 | Install Tile Flooring (x41) | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 52 |
| L16-7042 | Install Tile Flooring (x41) | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 53 |
| L12-8136 | Install Counter Subtops | 3 | 3 | 15-Sep-14 | 17-Sep-14 | 42 |
| L04-8206a | Install Base @ Corridors | 3 | 3 | 15-Sep-14 | 17-Sep-14 | 52 |
| L05-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 35 |
| L05-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 35 |
| L06-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 56 |
| L06-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 56 |
| MPP-1002 | Podium - Install Elevations 1 & 2 (west elevation, sou | 4 | 4 | 16-Sep-14 | 19-Sep-14 | 61 |
| MPP-1004 | Podium - Install Elevations 14-21 (Pool area) | 6 | 6 | 16-Sep-14 | 23-Sep-14 | 61 |
| MPP-1006 | Podium - Install Elevations 22-25 (Porte Cochere) | 6 | 6 | 16-Sep-14 | 23-Sep-14 | 61 |
| L12-8201 | Install ACT Grid @ Corridors | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 31 |
| L09-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 44 |
| L10-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 43 |
| L05-8418 | Flooring at Elevator Lobby | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 56 |
| L06-8418 | Flooring at Elevator Lobby | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 56 |
| L07-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 50 |
| L08-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 50 |
| L11-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 17-Sep-14 | 24-Sep-14 | 13 |
| L12-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 17-Sep-14 | 24-Sep-14 | 13 |
| L12-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 52 |
| L14-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 52 |
| L15-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 52 |
| L16-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 53 |
| L11-8138 | Install Toilet Accessories | 4 | 4 | 17-Sep-14 | 22-Sep-14 | 23 |
| L1BOH2-8104 | Prime Paint | 2 | 2 | 18-Sep-14 | 19-Sep-14 | 21 |
| I-1102 | Additional work at new L17 guest rooms | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 21 |

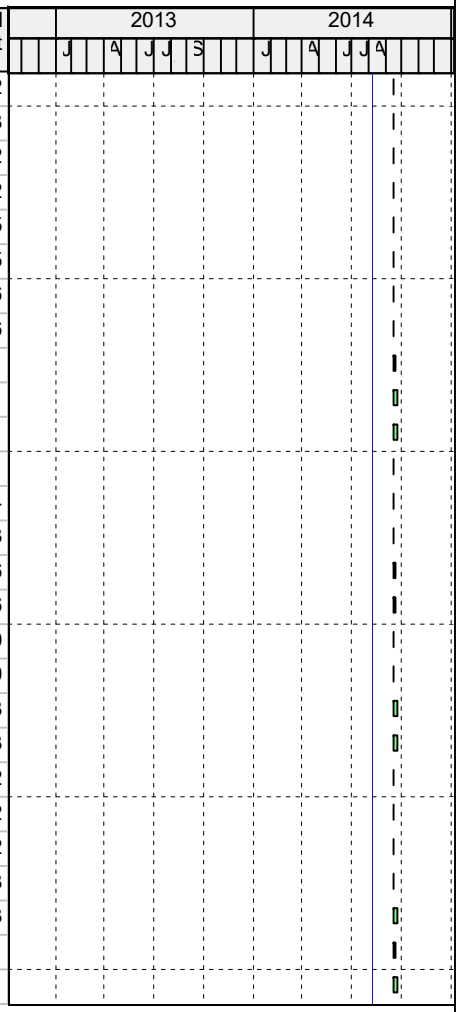



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 50 |
| L08-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 50 |
| L09-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 44 |
| L10-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 44 |
| L09-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 44 |
| L10-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 44 |
| L17-7042 | Install Tile Flooring (x41) | 2 | 2 | 18-Sep-14 | 19-Sep-14 | 49 |
| L14-8136 | Install Counter Subtops | 3 | 3 | 18-Sep-14 | 22-Sep-14 | 41 |
| L07-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 50 |
| L08-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 50 |
| L09-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 19-Sep-14 | 25-Sep-14 | 44 |
| L10-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 19-Sep-14 | 25-Sep-14 | 44 |
| L09-8405 | Cover Inspection | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 44 |
| L10-8405 | Cover Inspection | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 44 |
| L14-8129 | Install Shower Doors | 4 | 4 | 19-Sep-14 | 24-Sep-14 | 35 |
| L14-8201 | Install ACT Grid @ Corridors | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 32 |
| L06-8206a | Install Base @ Corridors | 3 | 3 | 19-Sep-14 | 23-Sep-14 | 48 |
| L1BOH2-8114 | T Bar Grid Ceiling | 3 | 3 | 22-Sep-14 | 24-Sep-14 | 21 |
| L11-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 45 |
| L14-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 30 |
| L17-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 49 |
| L03-8638 | Pool - Install pool deck and ADA lift | 3 | 3 | 22-Sep-14 | 24-Sep-14 | 27 |
| L08-8206a | Install Base @ Corridors | 3 | 3 | 22-Sep-14 | 24-Sep-14 | 50 |
| L07-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 50 |
| L08-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 50 |
| L12-8138 | Install Toilet Accessories | 4 | 4 | 23-Sep-14 | 26-Sep-14 | 26 |
| L15-8136 | Install Counter Subtops | 3 | 3 | 23-Sep-14 | 25-Sep-14 | 40 |

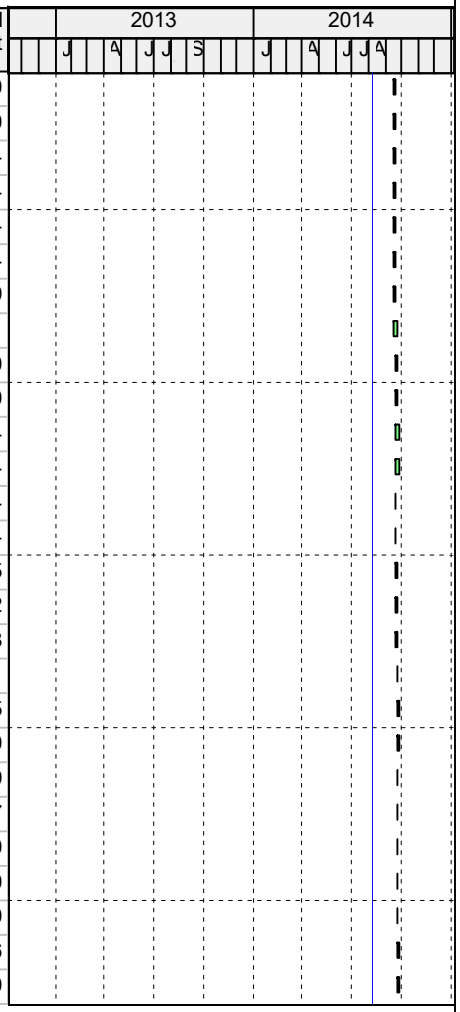



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 50 |
| L07-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 50 |
| L08-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 50 |
| L08-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 50 |
| L15-8201 | Install ACT Grid @ Corridors | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 34 |
| L07-8206a | Install Base @ Corridors | 3 | 3 | 24-Sep-14 | 26-Sep-14 | 45 |
| L11-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 25-Sep-14 | 25-Sep-14 | 38 |
| L12-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 25-Sep-14 | 25-Sep-14 | 37 |
| L07-8418 | Flooring at Elevator Lobby | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 50 |
| L08-8418 | Flooring at Elevator Lobby | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 50 |
| L09-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 25-Sep-14 | 25-Sep-14 | 44 |
| L10-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 25-Sep-14 | 25-Sep-14 | 44 |
| L14-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 25-Sep-14 | 02-Oct-14 | 13 |
| L15-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 25-Sep-14 | 02-Oct-14 | 13 |
| L15-8129 | Install Shower Doors | 4 | 4 | 25-Sep-14 | 30-Sep-14 | 35 |
| L03-8640 | Pool - Prep and install plaster | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 27 |
| L1BOH2C-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 21 |
| L1BOH2C-6014 | Complete Plumbing RI @ Ceilings & Inspection | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 21 |
| L1BOH2C-6016 | Complete Electrical RI @ Ceilings & Inspection | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 21 |
| L1BOH2C-6018 | Complete HVAC RI @ Ceilings & Inspection | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 21 |
| L1BOH2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 21 |
| L09-8206a | Install Base @ Corridors | 3 | 3 | 25-Sep-14 | 29-Sep-14 | 48 |
| L09-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 26-Sep-14 | 26-Sep-14 | 44 |
| L10-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 26-Sep-14 | 26-Sep-14 | 44 |
| L11-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 26-Sep-14 | 26-Sep-14 | 38 |
| L12-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 26-Sep-14 | 26-Sep-14 | 38 |
| L11-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 26-Sep-14 | 26-Sep-14 | 38 |

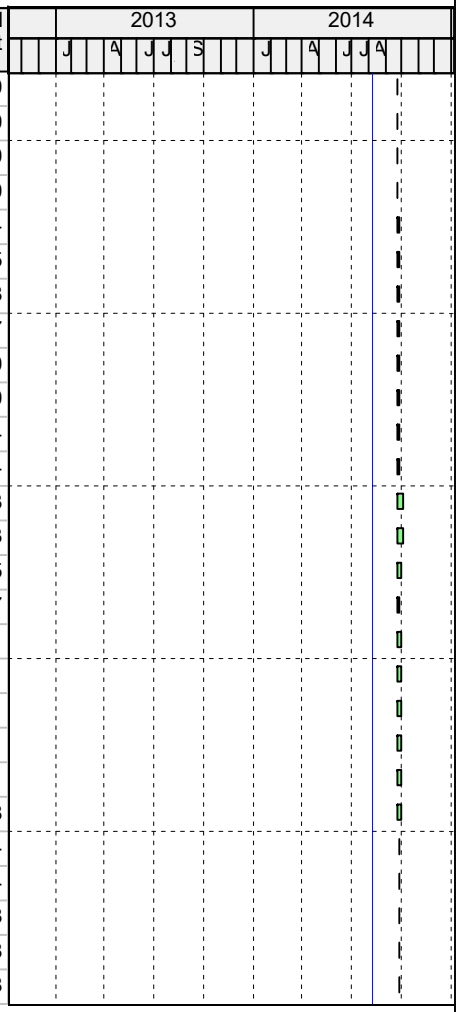



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 26-Sep-14 | 26-Sep-14 | 38 |
| L16-8136 | Install Counter Subtops | 3 | 3 | 26-Sep-14 | 30-Sep-14 | 39 |
| L10-8206a | Install Base @ Corridors | 3 | 3 | 27-Sep-14 | 30-Sep-14 | 56 |
| L09-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 44 |
| L10-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 44 |
| L11-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 38 |
| L12-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 38 |
| L11-8405 | Cover Inspection | 1 | 1 | 29-Sep-14 | 29-Sep-14 | 38 |
| L12-8405 | Cover Inspection | 1 | 1 | 29-Sep-14 | 29-Sep-14 | 38 |
| L03-8612 | L3 Pool - GWB hang/tape/finish | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 27 |
| L15-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 30 |
| L16-8201 | Install ACT Grid @ Corridors | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 33 |
| L03-8642 | Pool - Fill pool | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 53 |
| L14-8138 | Install Toilet Accessories | 4 | 4 | 29-Sep-14 | 02-Oct-14 | 26 |
| L09-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 01-Oct-14 | 01-Oct-14 | 44 |
| L10-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 01-Oct-14 | 01-Oct-14 | 44 |
| L16-8129 | Install Shower Doors | 4 | 4 | 01-Oct-14 | 06-Oct-14 | 35 |
| L03-8644 | Pool - Start-up and adjust pool equipment | 2 | 2 | 01-Oct-14 | 02-Oct-14 | 53 |
| L1B-8102a | GWB Hang/Tape (Ceilings) | 12 | 12 | 01-Oct-14 | 16-Oct-14 | 8 |
| L1BOH2-8140 | Acoustical Ceiling Tile | 4 | 4 | 02-Oct-14 | 07-Oct-14 | 21 |
| L09-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 44 |
| L09-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 44 |
| L10-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 44 |
| L10-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 44 |
| L03-8206a | Install Base @ Corridors | 3 | 3 | 02-Oct-14 | 06-Oct-14 | 39 |
| L14-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 32 |
| L15-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 19 |

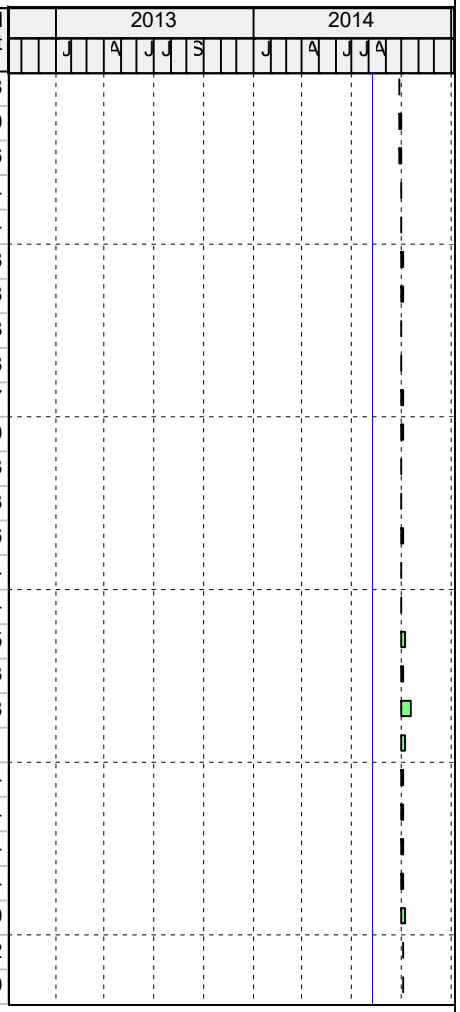



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8418 | Flooring at Elevator Lobby | 2 | 2 | 03-Oct-14 | 06-Oct-14 | 44 |
| L10-8418 | Flooring at Elevator Lobby | 2 | 2 | 03-Oct-14 | 06-Oct-14 | 44 |
| L11-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 38 |
| L12-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 38 |
| L16-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 03-Oct-14 | 10-Oct-14 | 13 |
| L17-8395 | Framing/GWB at Elevator Lobby Shaft Wall | 6 | 6 | 03-Oct-14 | 10-Oct-14 | 13 |
| L03-8646 | Pool - Health inspections | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 53 |
| L15-8138 | Install Toilet Accessories | 4 | 4 | 03-Oct-14 | 08-Oct-14 | 26 |
| L17-8136 | Install Counter Subtops | 3 | 3 | 03-Oct-14 | 07-Oct-14 | 36 |
| L11-8206a | Install Base @ Corridors | 3 | 3 | 04-Oct-14 | 07-Oct-14 | 25 |
| L11-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 38 |
| L12-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 38 |
| L14-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 32 |
| L15-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 20 |
| L14-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 32 |
| L15-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 20 |
| L1K-8340 | Install walk-in cooler/freezer (BY OTHERS) | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 11 |
| L03-8614 | L3 Pool - Paint/wall finishes | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 29 |
| L03-8618 | L3 Pool - Ceramic tile | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 27 |
| L16-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 30 |
| L17-8201 | Install ACT Grid @ Corridors | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 33 |
| L11-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 38 |
| L12-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 38 |
| L14-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 32 |
| L15-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 20 |
| L14-8405 | Cover Inspection | 1 | 1 | 07-Oct-14 | 07-Oct-14 | 32 |
| L15-8405 | Cover Inspection | 1 | 1 | 07-Oct-14 | 07-Oct-14 | 20 |

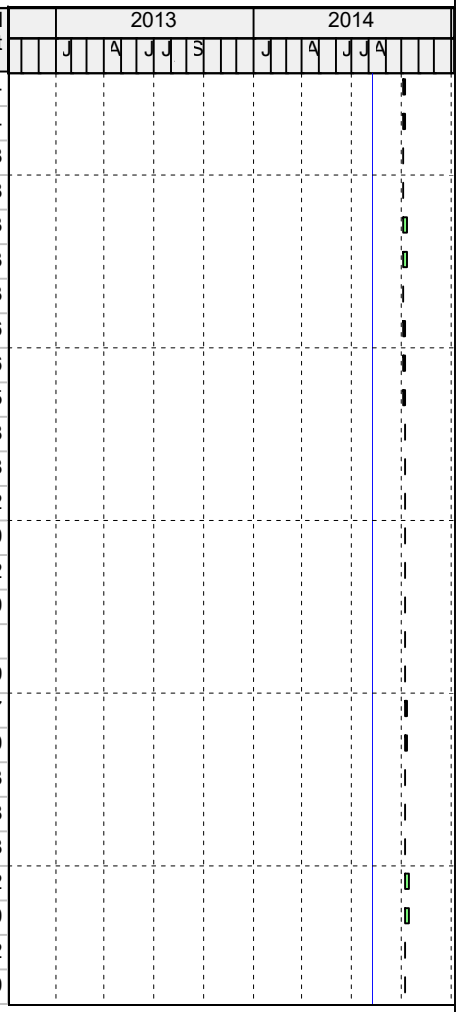



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 11 |
| L17-8129 | Install Shower Doors | 4 | 4 | 07-Oct-14 | 10-Oct-14 | 35 |
| L1BOH2-8200 | First Coat Finish Paint | 5 | 5 | 08-Oct-14 | 14-Oct-14 | 21 |
| LL1-8124a | Install Base | 3 | 3 | 08-Oct-14 | 10-Oct-14 | 32 |
| L11-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 38 |
| L12-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 38 |
| L16-8138 | Install Toilet Accessories | 4 | 4 | 09-Oct-14 | 14-Oct-14 | 26 |
| L11-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 38 |
| L11-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 38 |
| L12-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 38 |
| L12-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 38 |
| L12-8206a | Install Base @ Corridors | 3 | 3 | 11-Oct-14 | 14-Oct-14 | 25 |
| L16-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 13-Oct-14 | 13-Oct-14 | 14 |
| L17-8400 | Frame Ceilings/Furred Wall at Elevator Lobby | 1 | 1 | 13-Oct-14 | 13-Oct-14 | 13 |
| L11-8418 | Flooring at Elevator Lobby | 2 | 2 | 13-Oct-14 | 14-Oct-14 | 38 |
| L12-8418 | Flooring at Elevator Lobby | 2 | 2 | 13-Oct-14 | 14-Oct-14 | 38 |
| L14-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 13-Oct-14 | 13-Oct-14 | 32 |
| L15-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 13-Oct-14 | 13-Oct-14 | 20 |
| LL1-Z3-8340 | Install walk-in cooler/freezer (BY OTHERS) | 5 | 5 | 13-Oct-14* | 17-Oct-14 | 32 |
| L03-8620 | L3 Pool - Plumbing Fixtures & Trim / Finish | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 27 |
| L03-8622 | L3 Pool - HVAC trim / Finish | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 27 |
| L03-8624 | L3 Pool - Fire Sprinkler Trim / Finish | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 27 |
| L03-8626 | L3 Pool - Elec Trim/ Finish | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 27 |
| L03-8628 | L3 Pool - Elec Specialties Trim / Finish | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 27 |
| L17-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 30 |
| LL1-Z2-8124a | Install Base | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 24 |
| L14-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 14-Oct-14 | 14-Oct-14 | 32 |

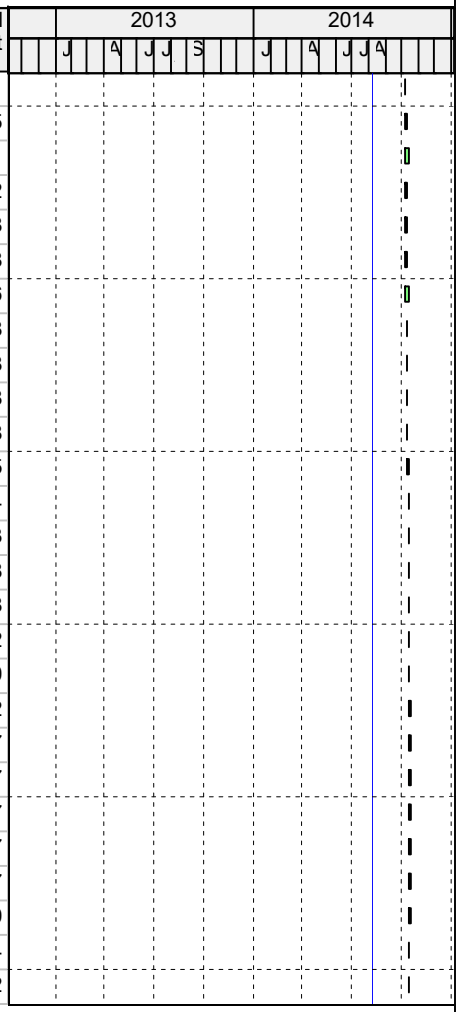



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 14-Oct-14 | 14-Oct-14 | 20 |
| L16-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 14-Oct-14 | 14-Oct-14 | 14 |
| L17-8402 | Electrical Rough-In at Elevator Lobby | 1 | 1 | 14-Oct-14 | 14-Oct-14 | 13 |
| LL1-Z2-8108 | Install Junior Balllroom ceiling feature (allowance) | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 24 |
| L16-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 14-Oct-14 | 14-Oct-14 | 14 |
| L17-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 1 | 14-Oct-14 | 14-Oct-14 | 13 |
| L1BOH2-8124 | Flooring | 4 | 4 | 15-Oct-14 | 20-Oct-14 | 21 |
| L14-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 15-Oct-14 | 16-Oct-14 | 32 |
| L15-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 15-Oct-14 | 16-Oct-14 | 20 |
| L16-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 14 |
| L17-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 13 |
| L16-8405 | Cover Inspection | 1 | 1 | 15-Oct-14 | 15-Oct-14 | 14 |
| L17-8405 | Cover Inspection | 1 | 1 | 15-Oct-14 | 15-Oct-14 | 13 |
| L17-8138 | Install Toilet Accessories | 4 | 4 | 15-Oct-14 | 20-Oct-14 | 26 |
| L14-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 17-Oct-14 | 17-Oct-14 | 32 |
| L15-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 17-Oct-14 | 17-Oct-14 | 20 |
| CO-7100T | CO - Preliminary Start-Up & Testing (Tower) | 10 | 10 | 17-Oct-14 | 30-Oct-14 | 13 |
| L1L-8102a | GWB Hang/Tape (Ceilings) | 11 | 11 | 17-Oct-14 | 31-Oct-14 | 0 |
| L14-8206a | Install Base @ Corridors | 3 | 3 | 18-Oct-14 | 21-Oct-14 | 25 |
| L14-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 20-Oct-14 | 20-Oct-14 | 32 |
| L14-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 20-Oct-14 | 20-Oct-14 | 32 |
| L15-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 20-Oct-14 | 20-Oct-14 | 20 |
| L15-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 20-Oct-14 | 20-Oct-14 | 20 |
| LL1-Z2-8118a | Install decorative light fixtures | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 29 |
| LL1-Z3-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 20-Oct-14* | 21-Oct-14 | 32 |
| L03-8630 | L3 Pool - Doors & Hardware | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 27 |
| L1BOH2-8124a | Install Base | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 21 |

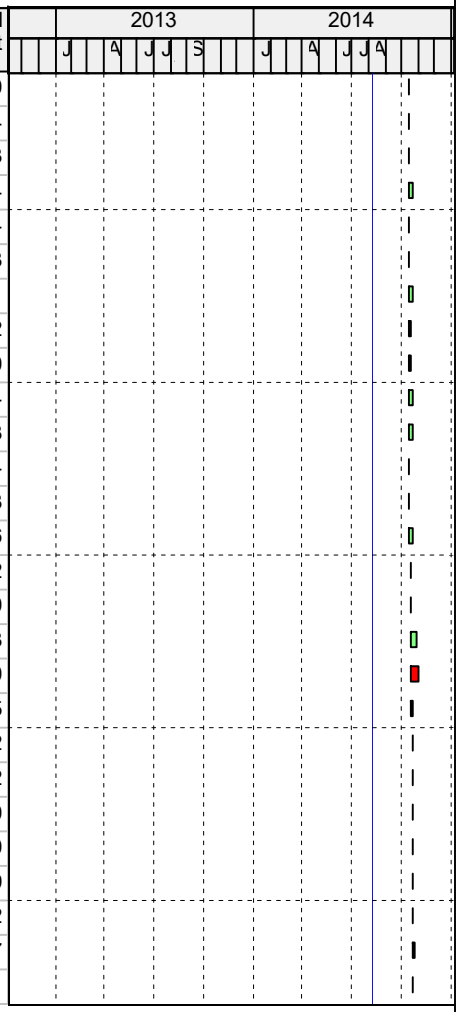



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8418 | Flooring at Elevator Lobby | 2 | 2 | 21-Oct-14 | 22-Oct-14 | 32 |
| L15-8418 | Flooring at Elevator Lobby | 2 | 2 | 21-Oct-14 | 22-Oct-14 | 32 |
| L16-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 21-Oct-14 | 21-Oct-14 | 14 |
| L17-8406 | Primer Paint Coat at Elevator Lobby | 1 | 1 | 21-Oct-14 | 21-Oct-14 | 13 |
| L1BOH2-8116 | Finish Carpentry / Millwork | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 21 |
| L1BOH2-8126 | Doors & Hardware | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 23 |
| L16-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 22-Oct-14 | 22-Oct-14 | 14 |
| L17-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 22-Oct-14 | 22-Oct-14 | 13 |
| L16-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 14 |
| L17-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 13 |
| L1K-8124a | Install Flooring (Epoxy) | 8 | 8 | 23-Oct-14 | 31-Oct-14 | 13 |
| L15-8206a | Install Base @ Corridors | 3 | 3 | 25-Oct-14 | 28-Oct-14 | 32 |
| L16-8206a | Install Base @ Corridors | 3 | 3 | 25-Oct-14 | 28-Oct-14 | 26 |
| L1BOH2-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 23 |
| L1BOH2-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 23 |
| L1BOH2-8204 | Mech Trim / Finish (HVAC & Plumbing) | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 21 |
| L16-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 27-Oct-14 | 27-Oct-14 | 14 |
| L17-8412 | Final Coat Finish Paint at Elevator Lobby | 1 | 1 | 27-Oct-14 | 27-Oct-14 | 13 |
| L03-8632 | L3 Pool - Install Bathroom Accessories | 3 | 3 | 27-Oct-14 | 29-Oct-14 | 27 |
| L16-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 28-Oct-14 | 28-Oct-14 | 14 |
| L16-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 28-Oct-14 | 28-Oct-14 | 14 |
| L17-8414 | Elec Trim / Finish at Elevator Lobby | 1 | 1 | 28-Oct-14 | 28-Oct-14 | 13 |
| L17-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 28-Oct-14 | 28-Oct-14 | 14 |
| L1BOH2-8201 | Final Coat Finish Paint | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 23 |
| L16-8418 | Flooring at Elevator Lobby | 2 | 2 | 29-Oct-14 | 30-Oct-14 | 26 |
| L17-8418 | Flooring at Elevator Lobby | 2 | 2 | 29-Oct-14 | 30-Oct-14 | 26 |
| CO-7102T | CO - HVAC Commissioning (Tower) | 5 | 5 | 31-Oct-14 | 06-Nov-14 | 29 |

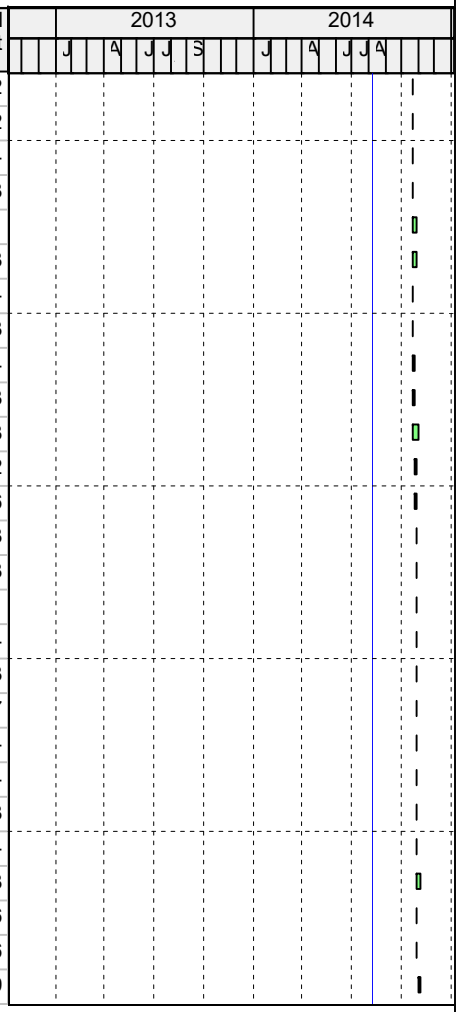



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7110T | Fire Sprinkler Pre-Testing (Tower) | 5 | 5 | 31-Oct-14 | 06-Nov-14 | 24 |
| CO-7116T | Fire Alarm Pre-Testing (Tower) | 5 | 5 | 31-Oct-14 | 06-Nov-14 | 24 |
| CO-7104T | Smoke Control Pre-Testing (Tower) | 5 | 5 | 31-Oct-14 | 06-Nov-14 | 24 |
| L17-8206a | Install Base @ Corridors | 3 | 3 | 01-Nov-14 | 04-Nov-14 | 26 |
| L1K-8124b | Install Base | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 15 |
| L1BOH2-8134 | Clean | 4 | 4 | 05-Nov-14 | 11-Nov-14 | 23 |
| L1BOH2-8132 | Punch | 4 | 4 | 05-Nov-14 | 11-Nov-14 | 23 |
| I-3102 | Ballroom ceilings - additional work per ASIs 18, 25 | 4 | 4 | 06-Nov-14 | 12-Nov-14 | 11 |
| L1B-8120 | Install operable partitions | 3 | 3 | 06-Nov-14 | 11-Nov-14 | 12 |
| L1B-8128 | Install Base | 2 | 2 | 06-Nov-14 | 07-Nov-14 | 13 |
| CO-7112T | City of Bellevue Fire Sprinkler Inspection / Approval (T | 5 | 5 | 07-Nov-14 | 14-Nov-14 | 24 |
| CO-7118T | City of Bellevue Fire Alarm Inspection / Approval (Tow | 5 | 5 | 07-Nov-14 | 14-Nov-14 | 24 |
| CO-7106T | City of Bellevue Smoke Control Testing (Tower) | 5 | 5 | 07-Nov-14 | 14-Nov-14 | 24 |
| L1BOH2-8210 | Owner Walk / Create Punchlist | 1 | 1 | 12-Nov-14 | 12-Nov-14 | 23 |
| L1BOH2-8212 | Resolve Final Punchlist | 3 | 3 | 13-Nov-14 | 17-Nov-14 | 23 |
| I-1602 | Enclosure at manlift - Framing & windows | 6 | 6 | 14-Nov-14 | 21-Nov-14 | 14 |
| L1BOH2-81214 | L1, Zone 3 Complete | 0 | 0 | | 17-Nov-14 | 23 |
| I-1604 | Enclosure at manlift - GWB | 6 | 6 | 19-Nov-14 | 26-Nov-14 | 14 |
| I-1606 | Enclosure at manlift - Paint & finishes | 4 | 4 | 21-Nov-14 | 26-Nov-14 | 14 |
| I-1608 | Enclosure at manlift - Metal panels | 6 | 6 | 21-Nov-14 | 02-Dec-14 | 14 |
| L1K-8128 | Install Kitchen equipment (BY OTHERS) | 10 | 10 | 24-Nov-14 | 09-Dec-14 | 9 |
| L1L-8124a | Install Base | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 2 |
| I-1202 | Concierge Lounge - Additional flooring work | 1 | 1 | 25-Nov-14 | 25-Nov-14 | 0 |
| I-1204 | Concierge Lounge - Additional millwork | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 0 |
| L1L-8120 | Install plumbing at bar | 2 | 2 | 25-Nov-14 | 26-Nov-14 | 2 |
| L1L-8122 | Install electrical at bar | 2 | 2 | 25-Nov-14 | 26-Nov-14 | 2 |
| CO-7124 | Complete Final Building Inspections | 5 | 5 | 23-Dec-14 | 31-Dec-14 | 0 |

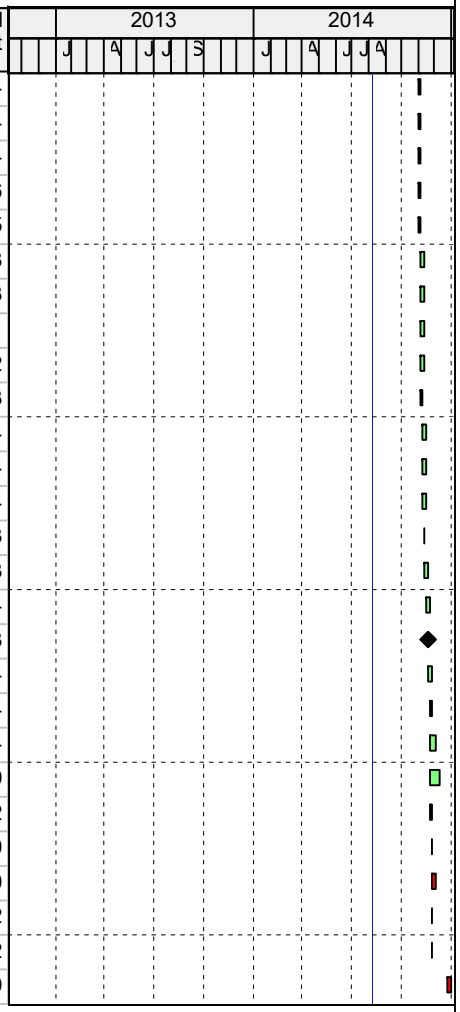


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13 A | | |
| CM-1002 | CM - Contract Time (578 Cal Days) | 576 | 59 | 06-Mar-13 A | 05-Oct-14 | 87 |
| CM-1014 | CM - Start of Construction | 0 | 0 | 05-Apr-13 A | | |
| CM-1006 | Construction Documents Issued by Client - (Due on 7 | 0 | 0 | 08-Aug-14 | | 146 |
| CM-1008 | Finalization of Allowances - (Due on 9-2-13) | 0 | 0 | 08-Aug-14 | | 146 |
| CO-7004 | CO - Prep / Submit O&M Manuals | 40 | 40 | 27-Sep-14 | 05-Nov-14 | 56 |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 31-Oct-14 | | 20 |
| CM-1016 | CM - Owner FF+E "Build-Out" | 42 | 42 | 31-Oct-14 | 11-Dec-14 | 20 |
| CM-1018 | CM - Hotel Operations Training | 21 | 21 | 15-Nov-14* | 05-Dec-14 | 26 |
| CO-7006 | CO - Certificate of Occupancy/Substantial Completior | 0 | 0 | | 31-Dec-14 | 0 |
| CO-7122 | CO - Certificate of Occupancy | 0 | 0 | | 31-Dec-14 | 0 |
| **Misc Milestones** | | | | | | |
| CM-1020 | MM - Site Mobilization | 10 | 0 | 06-Mar-13 A | 04-Apr-13 A | |
| MM-1008 | MM - Top Out - Tower / Structure | 0 | 0 | | 16-Apr-14 A | |
| MM-1004 | MM - Start Drywall In Tower | 0 | 0 | 27-Jun-14 A | | |
| MM-1010 | Energize Permanent Power | 5 | 5 | 08-Aug-14 | 12-Aug-14 | 111 |
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 22-Sep-14 | 60 |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| **Tower Crane** | | | | | | |
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 0 | 04-Jun-13 A | 14-Jun-13 A | |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 0 | 20-Jun-13 A | 24-Jun-13 A | |
| TC-5902 | Tower Crane - Erectiion | 2 | 0 | 21-Jun-13 A | 24-Jun-13 A | |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 24-Jun-13 A | | |

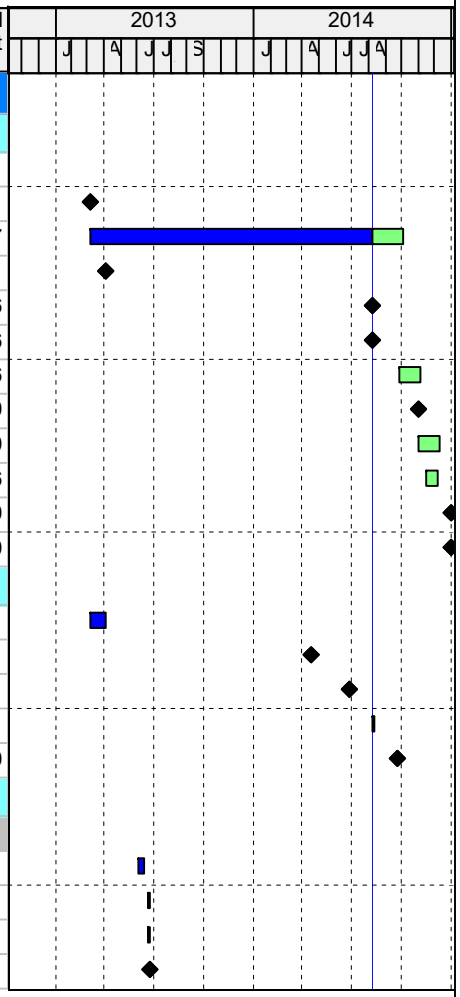


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| TC-5906 | Tower Crane - Operatational Period | 391 | 0 | 24-Jun-13 A | 16-Jun-14 A | |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 0 | 16-Jun-14 A | 17-Jun-14 A | |
| **Man & Material Lifts** | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 0 | 14-Jan-14 A | 20-Jan-14 A | |
| ML-5952 | Man/Material Lifts - Erect/Build Loading Dock | 5 | 0 | 21-Jan-14 A | 27-Jan-14 A | |
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 10-Feb-14 A | | |
| ML-5954 | Man/Material Lifts - Load Test / Certify | 1 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| ML-5958 | Man/Material Lifts - Operatational Period | 196 | 90 | 10-Feb-14 A | 05-Nov-14 | 25 |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 5 | 5 | 06-Nov-14 | 13-Nov-14 | 14 |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |
| **Mass Excavation / Shoring** | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 0 | 05-Apr-13 A | 12-Apr-13 A | |
| SW-2002 | Demolition And Utility Relocation | 8 | 0 | 15-Apr-13 A | 19-Apr-13 A | |
| SW-2010 | Grade Subgrade for Elect/Plumbing | 3 | 0 | 07-Jan-14 A | 09-Jan-14 A | |
| **Site Finishes** | | | | | | |
| SW-2006 | Install Perm Power Electrical Service / Dry Utilities (Ofl | 15 | 0 | 20-May-14 A | 05-Jun-14 A | |
| SW-2004 | Offsite Water & Water Connection | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 69 |
| SW-2008 | Sidewalks / Landscaping / Street Improvements | 40 | 40 | 25-Sep-14 | 25-Nov-14 | 13 |
| **Structure** | | | | | | |
| **Foundation / Substructure - (Levels LL4 / LL3)** | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 0 | 12-Jun-13 A | 27-Jun-13 A | |
| LL4-1601 | LL4 - Excavate Footings | 14 | 0 | 17-Jun-13 A | 30-Jul-13 A | |
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 0 | 18-Jun-13 A | 24-Jun-13 A | |
| LL4-1606 | LL4 - Undrgmd Plumbing | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |

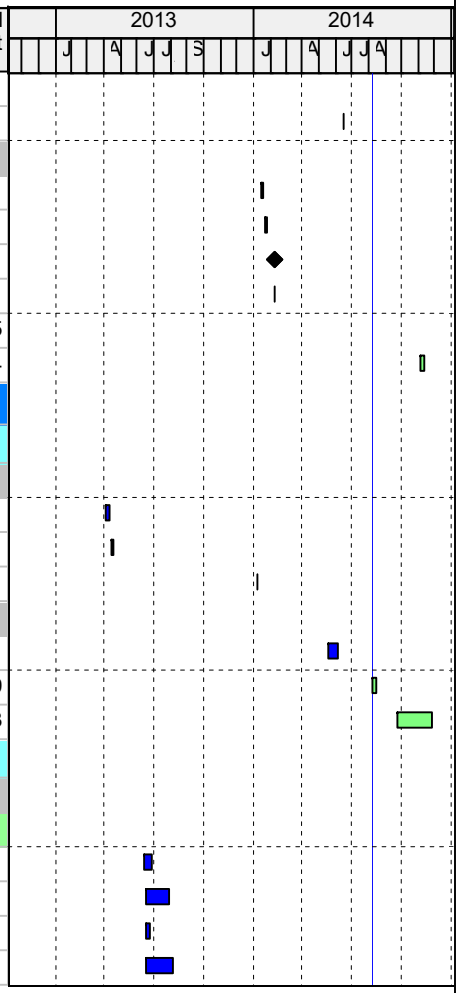



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-1608 | LL4 - Undrgrnd Elec | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 0 | 19-Jun-13 A | 25-Jun-13 A | |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 0 | 26-Jun-13 A | 02-Aug-13 A | |
| LL4-2033 | LL4 - Shotcrete Walls | 27 | 0 | 26-Jun-13 A | 05-Aug-13 A | |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 0 | 03-Jul-13 A | 21-Aug-13 A | |
| LL4-1614 | LL4 - FRP SOG | 5 | 0 | 10-Jul-13 A | 07-Aug-13 A | |
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 0 | 12-Jul-13 A | 26-Jul-13 A | |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 0 | 13-Jul-13 A | 06-Aug-13 A | |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 0 | 22-Jul-13 A | 24-Jul-13 A | |
| LL4-1618 | LL4 - FRP Ramp SOG | 5 | 0 | 01-Aug-13 A | 07-Aug-13 A | |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2004 | LL2 - Shore / Form Deck | 8 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2006 | LL3 - M & E Inserts | 4 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2008 | LL3 - ReSteel / PT Cables | 6 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2010 | LL3 - Install Embeds | 2 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2001 | LL3 - Waterproof Walls | 3 | 0 | 05-Aug-13 A | 05-Aug-13 A | |
| LL3-2012 | LL3 - Pour / Finish Deck | 2 | 0 | 16-Aug-13 A | 16-Aug-13 A | |
| LL3-2014 | LL3 - Stress Tendons | 1 | 0 | 19-Aug-13 A | 19-Aug-13 A | |
| LL3-2000 | LL3 - FRP Core Walls | 8 | 0 | 19-Aug-13 A | 28-Aug-13 A | |
| LL3-2033 | LL3 - Shotcrete Walls | 5 | 0 | 23-Aug-13 A | 26-Aug-13 A | |
| LL3-2016 | LL3 - Strip / ReShore Deck | 3 | 0 | 01-Sep-13 A | 13-Sep-13 A | |
| LL3-2018 | LL3 - Remove ReShores | 4 | 0 | 04-Nov-13 A | 07-Nov-13 A | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Grids 1 to 4 - (SOG @ Loading Dock)** | | | | | | |
| LL2-2056 | LL2 - Grease Intercepter | 5 | 0 | 15-Aug-13 A | 21-Aug-13 A | |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 0 | 27-Aug-13 A | 04-Sep-13 A | |

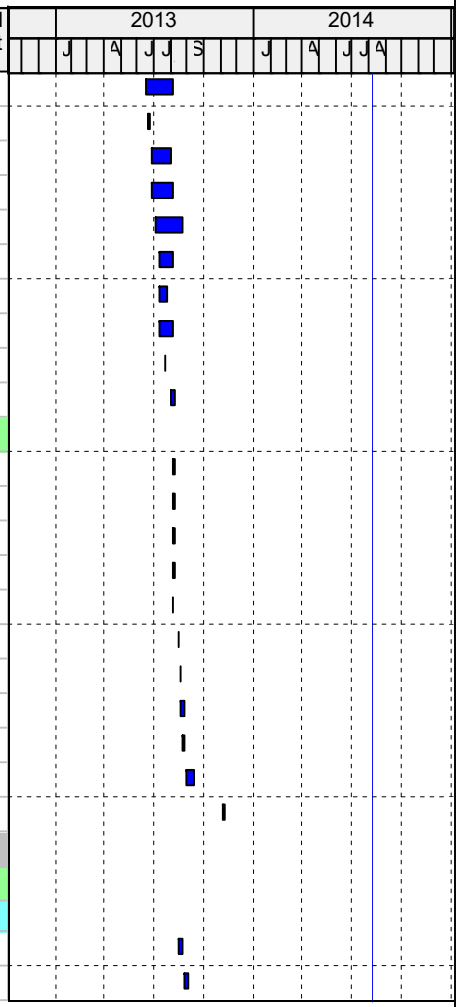


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2027 | LL2 - Waterproof Walls | 2 | 0 | 27-Aug-13 A | 28-Aug-13 A | |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 0 | 30-Aug-13 A | 05-Sep-13 A | |
| LL2-2021 | LL2 - FRP Elec Vault | 14 | 0 | 30-Aug-13 A | 04-Sep-13 A | |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 0 | 04-Sep-13 A | 11-Sep-13 A | |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 0 | 11-Sep-13 A | 13-Sep-13 A | |
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls/Roof | 11 | 0 | 19-Sep-13 A | 03-Oct-13 A | |
| LL2-2020 | LL2 - Undrgmd Plumbing | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2022 | LL2 - Undrgmd Elec | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2031 | LL2 - FRP Generator SOG | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2015 | LL2 to LL1 FRP Columns / Misc Walls | 6 | 0 | 01-Oct-13 A | 01-Oct-13 A | |
| LL2-2029 | LL2 - F/R/P Pour #2 | 8 | 0 | 15-Jan-14 A | 24-Jan-14 A | |
| LL2-2011 | LL2 - F/R/P Pour #3 | 16 | 0 | 24-Jan-14 A | 18-Feb-14 A | |
| LL2-2019 | LL2 - F/R/P Pour #6 | 4 | 0 | 19-Feb-14 A | 17-Mar-14 A | |
| LL2-2044 | LL2 - Set Generator | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |
| LL2-2004 | LL2 - Shore / Form Deck | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2035 | LL2 to LL1 - Shotcrete Walls | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2006 | LL2 - M & E Inserts | 4 | 0 | 14-Aug-13 A | 19-Aug-13 A | |
| LL2-2008 | LL2 - ReSteel / PT Cables | 6 | 0 | 14-Aug-13 A | 21-Aug-13 A | |
| LL2-2010 | LL2 - Install Embeds | 3 | 0 | 14-Aug-13 A | 16-Aug-13 A | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 0 | 27-Aug-13 A | 06-Sep-13 A | |
| LL2-2012 | LL2 - Place / Finish Deck | 3 | 0 | 29-Aug-13 A | 29-Aug-13 A | |
| LL2-2023 | LL2 - Waterproof Walls | 3 | 0 | 29-Aug-13 A | 03-Sep-13 A | |
| LL2-2014 | LL2 - Stress Tendons | 1 | 0 | 30-Aug-13 A | 30-Aug-13 A | |
| LL2-2016 | LL2 - Strip / ReShore | 3 | 0 | 03-Sep-13 A | 05-Sep-13 A | |
| LL2-8234 | LL2 - Place / Finish Deck | 3 | 0 | 12-Sep-13 A | 12-Sep-13 A | |

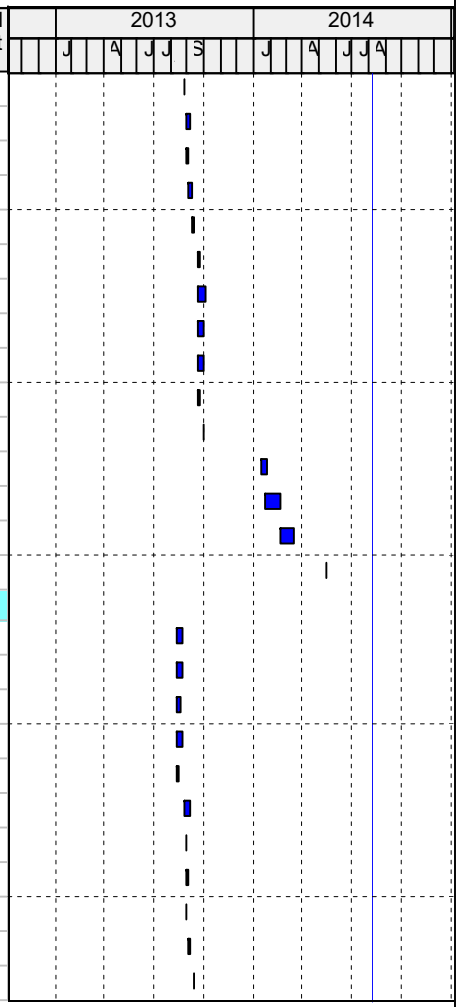


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2000 | LL2 - FRP Core Walls | 8 | 0 | 12-Sep-13 A | 23-Sep-13 A | |
| LL2-2018 | LL2 - Remove ReShores | 4 | 0 | 13-Nov-13 A | 18-Nov-13 A | |
| LL2-2013 | LL2 - F/R/P Pour #1 | 4 | 0 | 13-Jan-14 A | 16-Jan-14 A | |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| P5A-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2000 | LL1 - FRP Core Walls | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2004 | LL1 - Shore / Form Deck | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| P6-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P6-2004 | LL1 - Shore / Form Deck | 7 | 0 | 16-Sep-13 A | 24-Sep-13 A | |
| P5A-2006 | LL1 - MEP Rough In | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2008 | LL1 - ReSteel / PT Cables | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2012 | LL1 - Place / Finish Deck | 0 | 0 | 20-Sep-13 A | | |
| P5A-2020 | LL1 - Waterproof Walls | 3 | 0 | 20-Sep-13 A | 24-Sep-13 A | |
| P5A-2014 | LL1 - Stress Tendons | 1 | 0 | 23-Sep-13 A | 23-Sep-13 A | |
| P5A-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2006 | LL1 - MEP Rough In | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2008 | LL1 - ReSteel / PT Cables | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 24-Sep-13 A | 25-Sep-13 A | |
| P6-2020 | LL1 - Waterproof Walls | 4 | 0 | 24-Sep-13 A | 27-Sep-13 A | |
| P5A-2033 | LL1 - Resteel/Shotcrete Walls | 3 | 0 | 25-Sep-13 A | 27-Sep-13 A | |
| P5B-2002 | LL1 - FRP Columns Below | 5 | 0 | 26-Sep-13 A | 02-Oct-13 A | |
| P5B-2004 | LL1 - Shore / Form Deck | 7 | 0 | 26-Sep-13 A | 04-Oct-13 A | |
| P6-2012 | LL1 - Place / Finish Deck | 0 | 0 | 27-Sep-13 A | | |
| P6-2014 | LL1 - Stress Tendons | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2033 | LL1 - Resteel/Shotcrete Walls | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 01-Oct-13 A | 03-Oct-13 A | |

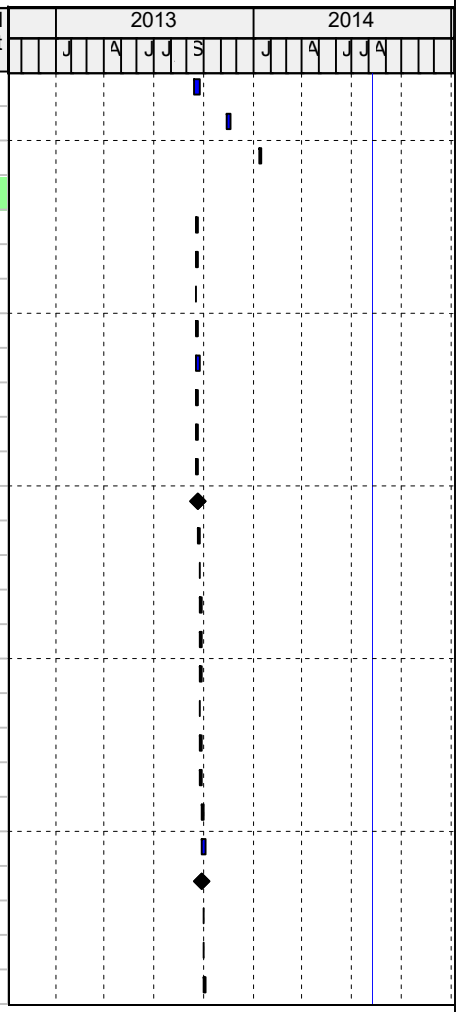



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P5B-2006 | LL1 - MEP Rough In | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2002 | FRP Columns Below | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2004 | Shore / Form Deck | 4 | 0 | 03-Oct-13 A | 08-Oct-13 A | |
| P5B-2008 | LL1 - ReSteel / PT Cables | 5 | 0 | 04-Oct-13 A | 10-Oct-13 A | |
| P5B-2010 | LL1 - Install Edgeform/Embeds | 4 | 0 | 04-Oct-13 A | 09-Oct-13 A | |
| P8-2002 | FRP Columns Below | 5 | 0 | 07-Oct-13 A | 11-Oct-13 A | |
| P8-2000 | Form/Resteel/Close Core Walls | 14 | 0 | 07-Oct-13 A | 24-Oct-13 A | |
| P8-2004 | Shore / Form Deck P8 | 8 | 0 | 07-Oct-13 A | 16-Oct-13 A | |
| P7-2002 | FRP Columns Below | 5 | 0 | 08-Oct-13 A | 14-Oct-13 A | |
| P7-2004 | Shore / Form Deck | 6 | 0 | 08-Oct-13 A | 15-Oct-13 A | |
| P10A--2006 | MEP Rough In | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2008 | ReSteel / PT Cables | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2010 | Install Edgeform/Embeds | 2 | 0 | 08-Oct-13 A | 09-Oct-13 A | |
| P5B-2012 | LL1 - Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P10A--2012 | Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P5B-2014 | LL1 - Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P7-2006 | MEP Rough In | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P7-2008 | ReSteel / PT Cables | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P10A--2014 | Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P8-2020 | Shore / Form Deck P9 | 6 | 0 | 14-Oct-13 A | 21-Oct-13 A | |
| P5B-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2010 | Install Edgeform/Embeds | 2 | 0 | 15-Oct-13 A | 16-Oct-13 A | |
| P8-2006 | MEP Rough In | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2008 | ReSteel / PT Cables | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2010 | Install Edgeform/Embeds | 4 | 0 | 15-Oct-13 A | 18-Oct-13 A | |
| P10A--2016 | Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2012 | Place / Finish Deck | 0 | 0 | 18-Oct-13 A | | |

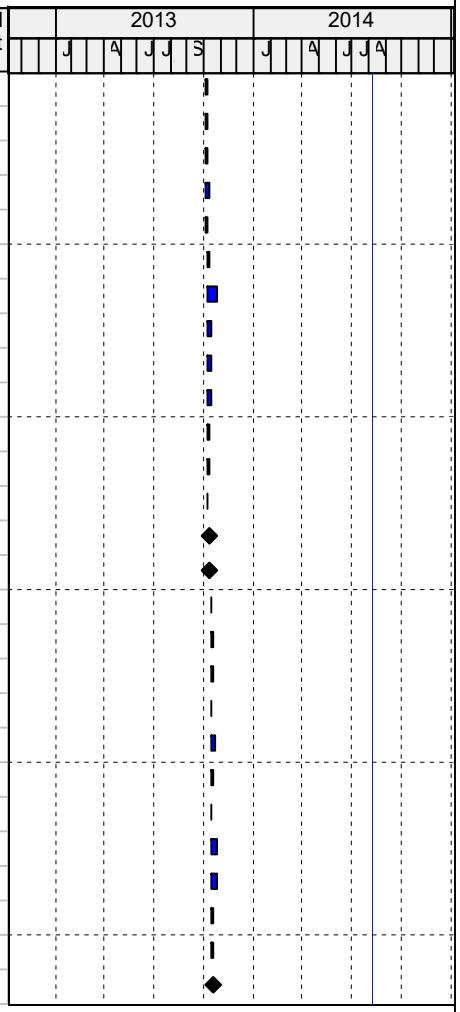



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P7-2033 | Resteel/Shotcrete Walls | 3 | 0 | 18-Oct-13 A | 22-Oct-13 A | |
| P7-2014 | Stress Tendons | 1 | 0 | 21-Oct-13 A | 21-Oct-13 A | |
| P7-2016 | Strip / ReShore Deck | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2002 | FRP Columns Below | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P10B--2000 | FRP Shear Walls Below | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2004 | Shore / Form Deck | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P8-2012 | Place / Finish Deck P 8 & 9 and Core Walls | 0 | 0 | 25-Oct-13 A | | |
| P8-2014 | Stress Tendons | 1 | 0 | 28-Oct-13 A | 28-Oct-13 A | |
| P10B--2006 | MEP Rough In | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2008 | ReSteel / PT Cables | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2010 | Install Edgeform/Embeds | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P12--2002 | FRP Columns Below | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P12--2000 | Form/Resteel/Close Core Walls | 9 | 0 | 28-Oct-13 A | 07-Nov-13 A | |
| P12--2004 | Shore / Form Deck | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P8-2016 | Strip / ReShore Deck | 3 | 0 | 29-Oct-13 A | 31-Oct-13 A | |
| P11--2002 | FRP Columns Below | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P11--2004 | Shore / Form Deck | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P10B--2012 | Place / Finish Deck | 0 | 0 | 31-Oct-13 A | | |
| P10B--2014 | Stress Tendons | 1 | 0 | 01-Nov-13 A | 01-Nov-13 A | |
| P12--2006 | MEP Rough In | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12--2008 | ReSteel / PT Cables | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12--2010 | Install Edgeform/Embeds | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P10B--2016 | Strip / ReShore Deck | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2006 | MEP Rough In | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2008 | ReSteel / PT Cables | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2010 | Install Edgeform/Embeds | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2012 | Place / Finish Deck | 0 | 0 | 07-Nov-13 A | | |

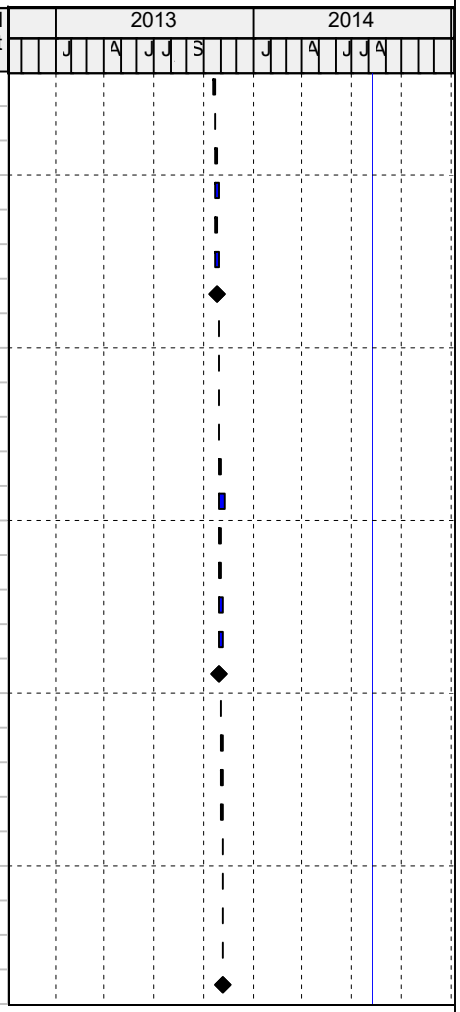


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P13–2002 | FRP Columns Below | 5 | 0 | 07-Nov-13 A | 14-Nov-13 A | |
| P13–2004 | Shore / Form Deck | 9 | 0 | 07-Nov-13 A | 28-Nov-13 A | |
| P11–2014 | Stress Tendons | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| P12–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 08-Nov-13 A | | |
| P11–2016 | Strip / ReShore Deck | 3 | 0 | 12-Nov-13 A | 14-Nov-13 A | |
| P12–2014 | Stress Tendons | 1 | 0 | 12-Nov-13 A | 12-Nov-13 A | |
| P14–2002 | FRP Columns Below | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P14–2000 | Form/Resteel/Close Core Walls | 8 | 0 | 19-Nov-13 A | 03-Dec-13 A | |
| P14–2004 | Shore / Form Deck | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P13A–2002 | FRP Columns Below | 5 | 0 | 21-Nov-13 A | 27-Nov-13 A | |
| P13A–2004 | Shore / Form Deck | 4 | 0 | 21-Nov-13 A | 26-Nov-13 A | |
| P13–2010 | Install Edgeform/Embeds | 5 | 0 | 22-Nov-13 A | 04-Dec-13 A | |
| P13–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2006 | MEP Rough In | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2010 | Install Edgeform/Embeds | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P13–2006 | MEP Rough In | 5 | 0 | 26-Nov-13 A | 03-Dec-13 A | |
| P13A–2006 | MEP Rough In | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2008 | ReSteel / PT Cables | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2010 | Install Edgeform/Embeds | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13–2012 | Place / Finish Deck | 0 | 0 | 02-Dec-13 A | | |
| P13A–2012 | Place / Finish Deck | 0 | 0 | 03-Dec-13 A | | |
| P14–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 04-Dec-13 A | | |
| P13–2014 | Stress Tendons | 1 | 0 | 05-Dec-13 A | 05-Dec-13 A | |
| P15–2002 | FRP Columns Below | 3 | 0 | 05-Dec-13 A | 09-Dec-13 A | |
| P15–2000 | Jump/Resteel/Close Core | 9 | 0 | 05-Dec-13 A | 17-Dec-13 A | |
| P15–2004 | Shore / Form Deck | 5 | 0 | 05-Dec-13 A | 11-Dec-13 A | |

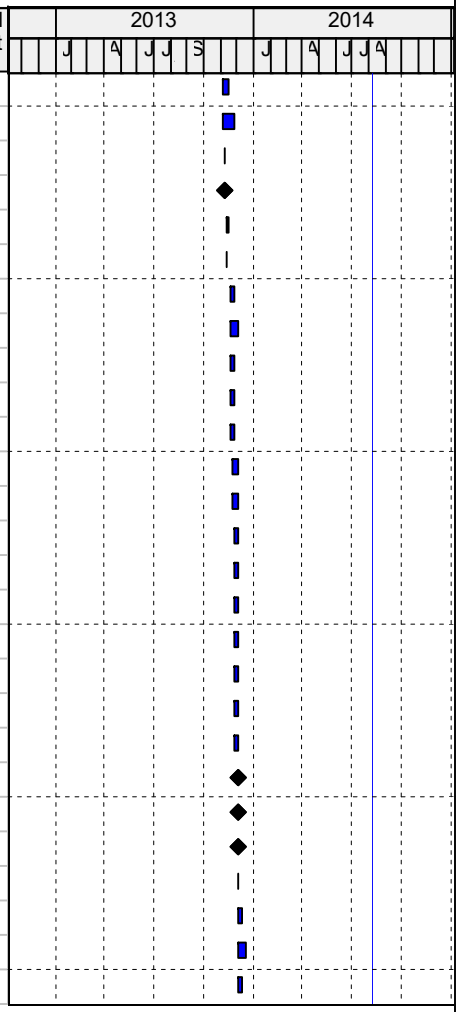



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P13–2016 | Strip / ReShore Deck | 3 | 0 | 06-Dec-13 A | 10-Dec-13 A | |
| P13A–2014 | Stress Tendons | 1 | 0 | 06-Dec-13 A | 06-Dec-13 A | |
| P14–2014 | Stress Tendons | 1 | 0 | 07-Dec-13 A | 07-Dec-13 A | |
| P15–2006 | MEP Rough In | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2008 | ReSteel / PT Cables | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2010 | Install Edgeform/Embeds | 3 | 0 | 11-Dec-13 A | 13-Dec-13 A | |
| P16-2002 | FRP Columns Below | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P16-2004 | Shore / Form Deck | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P15–2012 | Place / Finish Deck | 0 | 0 | 18-Dec-13 A | | |
| P15–2020 | Place Conc @ Core | 0 | 0 | 18-Dec-13 A | | |
| P16-2000 | Jump/Resteel/Close Core | 5 | 0 | 18-Dec-13 A | 24-Dec-13 A | |
| P16-2006 | MEP Rough In | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2008 | ReSteel / PT Cables | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2010 | Install Edgeform/Embeds | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P15–2014 | Stress Tendons | 1 | 0 | 21-Dec-13 A | 21-Dec-13 A | |
| P8-2018 | Remove Reshores | 2 | 0 | 23-Dec-13 A | 24-Dec-13 A | |
| P10A–2018 | Remove Reshores | 2 | 0 | 26-Dec-13 A | 27-Dec-13 A | |
| P16-2012 | Place / Finish Deck | 0 | 0 | 26-Dec-13 A | | |
| P16-2020 | Place Conc @ Core | 0 | 0 | 26-Dec-13 A | | |
| P17-2002 | FRP Columns Below | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P17-2000 | Jump/Resteel/Close Core | 7 | 0 | 27-Dec-13 A | 07-Jan-14 A | |
| P17-2004 | Shore / Form Deck | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P10B–2018 | Remove Reshores | 2 | 0 | 30-Dec-13 A | 31-Dec-13 A | |
| P16-2014 | Stress Tendons | 1 | 0 | 31-Dec-13 A | 31-Dec-13 A | |
| P5A-2018 | LL1 - Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P11–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P12–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |

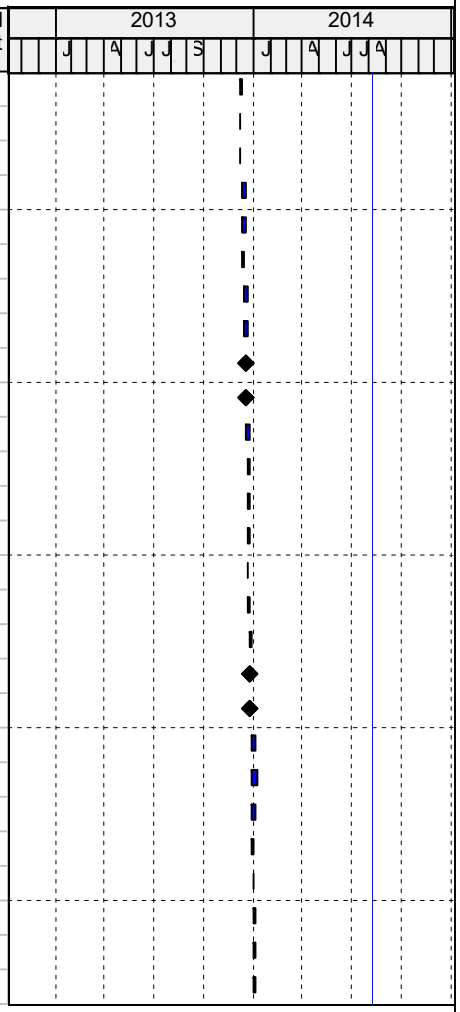


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P17-2006 | MEP Rough In | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2008 | ReSteel / PT Cables | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2010 | Install Edgeform/Embeds | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P6-2018 | LL1 - Remove Reshores | 2 | 0 | 06-Jan-14 A | 07-Jan-14 A | |
| P5B-2018 | LL1 - Remove Reshores | 2 | 0 | 08-Jan-14 A | 09-Jan-14 A | |
| P17-2012 | Place / Finish Deck | 0 | 0 | 08-Jan-14 A | | |
| P17-2020 | Place Conc @ Core | 0 | 0 | 08-Jan-14 A | | |
| P18-2002 | FRP Columns Below | 5 | 0 | 09-Jan-14 A | 15-Jan-14 A | |
| P18-2000 | Jump/Resteel/Close Core | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P18-2004 | Shore / Form Deck | 3 | 0 | 09-Jan-14 A | 13-Jan-14 A | |
| LL2-2022R | MEP Rough In | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P7-2018 | Remove Reshores | 2 | 0 | 10-Jan-14 A | 13-Jan-14 A | |
| P17-2014 | Stress Tendons | 1 | 0 | 11-Jan-14 A | 11-Jan-14 A | |
| P13–2018 | Remove Reshores | 2 | 0 | 13-Jan-14 A | 14-Jan-14 A | |
| P13A–2018 | Remove Reshores | 2 | 0 | 15-Jan-14 A | 16-Jan-14 A | |
| WEA-2012 | WIND IMPACT | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| P18-2006 | MEP Rough In | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2008 | ReSteel / PT Cables | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2010 | Install Edgeform/Embeds | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2012 | Place / Finish Deck | 0 | 0 | 22-Jan-14 A | | |
| P18-2020 | Place Conc @ Core | 0 | 0 | 22-Jan-14 A | | |
| P19-2002 | FRP Columns Below | 5 | 0 | 23-Jan-14 A | 29-Jan-14 A | |
| P19-2000 | Jump/Resteel/Close Core | 4 | 0 | 23-Jan-14 A | 28-Jan-14 A | |
| P19-2004 | Shore / Form Deck | 3 | 0 | 23-Jan-14 A | 27-Jan-14 A | |
| P18-2014 | Stress Tendons | 1 | 0 | 25-Jan-14 A | 25-Jan-14 A | |
| P14–2018 | Remove Reshores | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2006 | MEP Rough In | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |

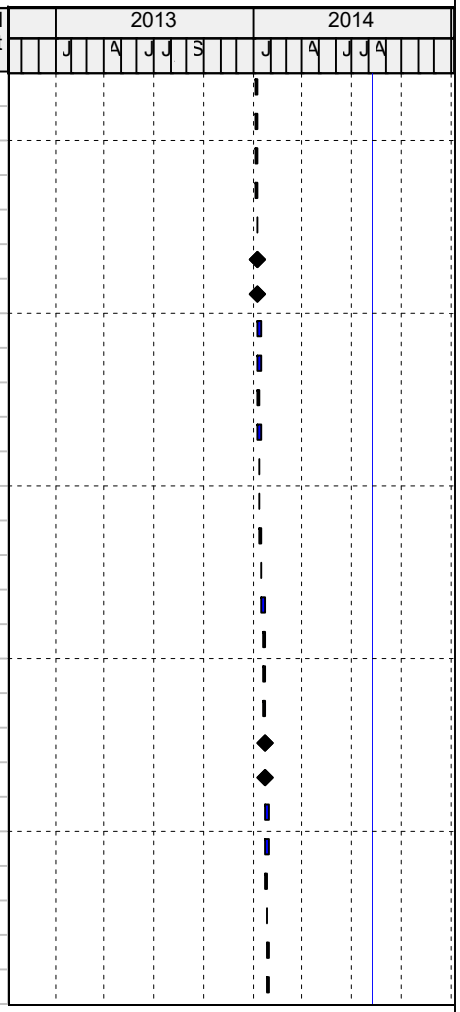



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P19-2008 | ReSteel / PT Cables | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2010 | Install Edgeform/Embeds | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2012 | Place / Finish Deck | 0 | 0 | 29-Jan-14 A | | |
| P19-2020 | Place Conc @ Core | 0 | 0 | 29-Jan-14 A | | |
| P20-2002 | FRP Columns Below | 5 | 0 | 30-Jan-14 A | 05-Feb-14 A | |
| P20-2000 | Jump/Resteel/Close Core | 9 | 0 | 30-Jan-14 A | 11-Feb-14 A | |
| P20-2004 | Shore / Form Deck | 6 | 0 | 30-Jan-14 A | 10-Feb-14 A | |
| P19-2014 | Stress Tendons | 1 | 0 | 01-Feb-14 A | 01-Feb-14 A | |
| P13A–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P14–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P15–2016 | Strip / ReShore Deck | 3 | 0 | 06-Feb-14 A | 10-Feb-14 A | |
| P20-2006 | MEP Rough In | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2008 | ReSteel / PT Cables | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2010 | Install Edgeform/Embeds | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| L03-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 06-Feb-14 A | 12-Feb-14 A | |
| P16-2016 | Strip / ReShore Deck | 3 | 0 | 10-Feb-14 A | 12-Feb-14 A | |
| L04-2018 | Remove Reshores | 2 | 0 | 10-Feb-14 A | 11-Feb-14 A | |
| L03-2018 | Remove Reshores | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| P17-2016 | Strip / ReShore Deck | 3 | 0 | 12-Feb-14 A | 14-Feb-14 A | |
| P20-2012 | Place / Finish Deck | 0 | 0 | 12-Feb-14 A | | |
| P20-2020 | Place Conc @ Core | 0 | 0 | 12-Feb-14 A | | |
| L04-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-Feb-14 A | 18-Feb-14 A | |
| P12–2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P18-2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P21-2002 | FRP Columns Below | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| P21-2000 | Jump/Resteel/Close Core | 4 | 0 | 13-Feb-14 A | 18-Feb-14 A | |
| P21-2004 | Shore / Form Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |

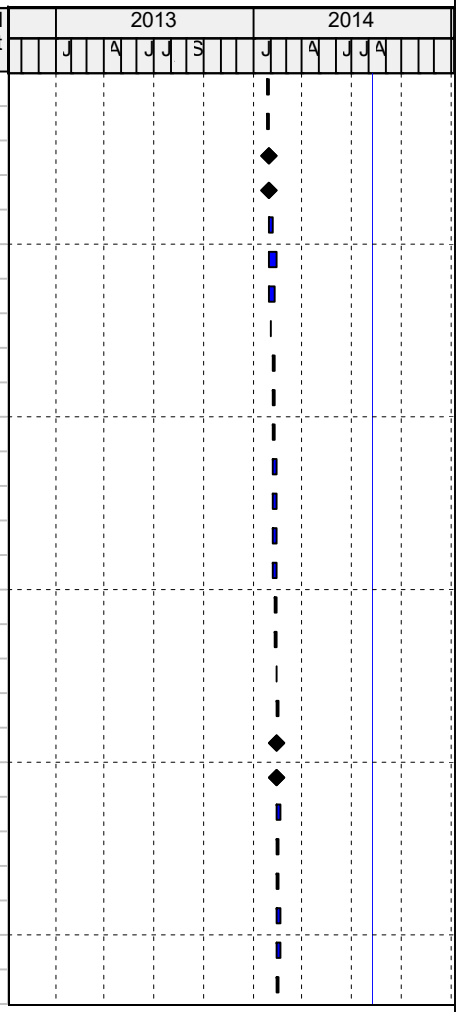



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P19-2016 | Strip / ReShore Deck | 3 | 0 | 14-Feb-14 A | 18-Feb-14 A | |
| P20-2014 | Stress Tendons | 1 | 0 | 15-Feb-14 A | 15-Feb-14 A | |
| P21-2006 | MEP Rough In | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2008 | ReSteel / PT Cables | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P20-2016 | Strip / ReShore Deck | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| L05-2018 | Remove Reshores | 2 | 0 | 18-Feb-14 A | 19-Feb-14 A | |
| P21-2012 | Place / Finish Deck | 0 | 0 | 19-Feb-14 A | | |
| P21-2020 | Place Conc @ Core | 0 | 0 | 19-Feb-14 A | | |
| P22-2002 | FRP Columns Below | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P22-2000 | Jump/Resteel/Close Core | 4 | 0 | 20-Feb-14 A | 25-Feb-14 A | |
| P22-2004 | Shore / Form Deck | 3 | 0 | 20-Feb-14 A | 24-Feb-14 A | |
| L05-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P21-2014 | Stress Tendons | 1 | 0 | 22-Feb-14 A | 22-Feb-14 A | |
| P21-2016 | Strip / ReShore Deck | 3 | 0 | 24-Feb-14 A | 26-Feb-14 A | |
| P22-2006 | MEP Rough In | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2008 | ReSteel / PT Cables | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| L06-2018 | Remove Reshores | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| P22-2012 | Place / Finish Deck | 0 | 0 | 26-Feb-14 A | | |
| P22-2020 | Place Conc @ Core | 0 | 0 | 26-Feb-14 A | | |
| P23-2002 | FRP Columns Below | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2000 | Jump/Resteel/Close Core | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2004 | Shore / Form Deck | 3 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2006 | MEP Rough In | 2 | 0 | 01-Mar-14 A | 03-Mar-14 A | |
| P22-2014 | Stress Tendons | 1 | 0 | 01-Mar-14 A | 01-Mar-14 A | |
| P23-2008 | ReSteel / PT Cables | 2 | 0 | 03-Mar-14 A | 04-Mar-14 A | |

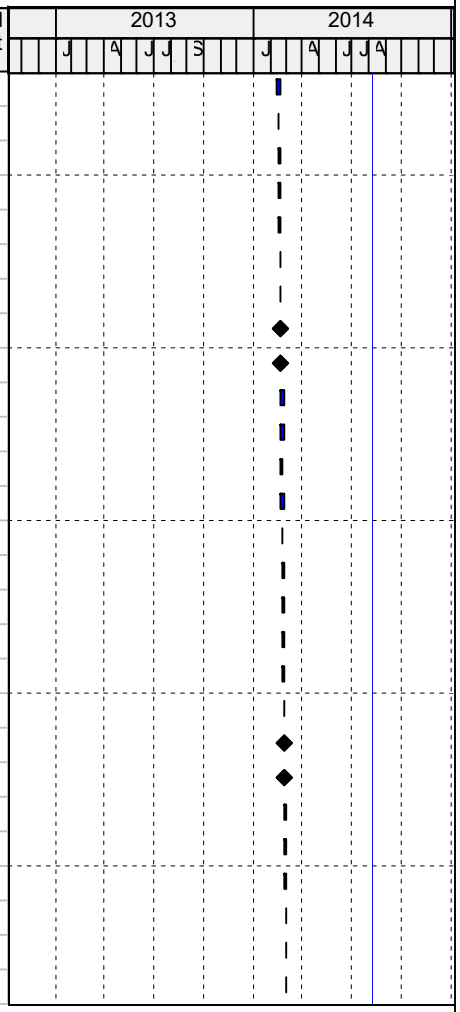



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P22-2016 | Strip / ReShore Deck | 3 | 0 | 04-Mar-14 A | 10-Mar-14 A | |
| P23-2010 | Install Edgeform/Embeds | 2 | 0 | 04-Mar-14 A | 04-Mar-14 A | |
| L07-2018 | Remove Reshores | 2 | 0 | 04-Mar-14 A | 05-Mar-14 A | |
| P23-2012 | Place / Finish Deck | 0 | 0 | 05-Mar-14 A | | |
| P23-2020 | Place Conc @ Core | 0 | 0 | 05-Mar-14 A | | |
| P24-2002 | FRP Columns Below | 5 | 0 | 05-Mar-14 A | 07-Mar-14 A | |
| P24-2004 | Shore / Form Deck | 3 | 0 | 06-Mar-14 A | 10-Mar-14 A | |
| P24-2000 | Jump/Resteel/Close Core | 4 | 0 | 08-Mar-14 A | 10-Mar-14 A | |
| P23-2014 | Stress Tendons | 1 | 0 | 10-Mar-14 A | 10-Mar-14 A | |
| P24-2008 | ReSteel / PT Cables | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P24-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P23-2016 | Strip / ReShore Deck | 3 | 0 | 11-Mar-14 A | 17-Mar-14 A | |
| P24-2006 | MEP Rough In | 2 | 0 | 11-Mar-14 A | 11-Mar-14 A | |
| P25-2002 | FRP Columns Below | 5 | 0 | 11-Mar-14 A | 13-Mar-14 A | |
| L08-2018 | Remove Reshores | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| P24-2012 | Place / Finish Deck | 0 | 0 | 12-Mar-14 A | | |
| P24-2020 | Place Conc @ Core | 0 | 0 | 12-Mar-14 A | | |
| P25-2004 | Shore / Form Deck | 3 | 0 | 13-Mar-14 A | 17-Mar-14 A | |
| P25-2000 | Jump/Resteel/Close Core | 4 | 0 | 15-Mar-14 A | 17-Mar-14 A | |
| P24-2014 | Stress Tendons | 1 | 0 | 17-Mar-14 A | 17-Mar-14 A | |
| P25-2006 | MEP Rough In | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2008 | ReSteel / PT Cables | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| L06-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 18-Mar-14 A | 20-Mar-14 A | |
| L09-2018 | Remove Reshores | 2 | 0 | 18-Mar-14 A | 19-Mar-14 A | |
| P26-2002 | FRP Columns Below | 5 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| P25-2012 | Place / Finish Deck | 0 | 0 | 19-Mar-14 A | | |

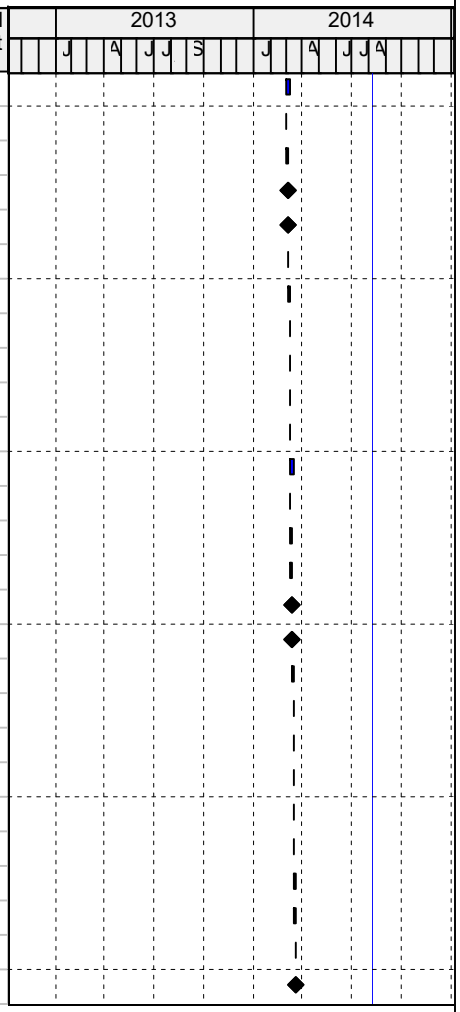



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P25-2020 | Place Conc @ Core | 0 | 0 | 19-Mar-14 A | | |
| P26-2004 | Shore / Form Deck | 3 | 0 | 20-Mar-14 A | 24-Mar-14 A | |
| L07-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 21-Mar-14 A | 25-Mar-14 A | |
| P26-2000 | Jump/Resteel/Close Core | 4 | 0 | 22-Mar-14 A | 24-Mar-14 A | |
| P26-2006 | MEP Rough In | 2 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P26-2008 | ReSteel / PT Cables | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P26-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P25-2014 | Stress Tendons | 1 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P27-2002 | FRP Columns Below | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| P26-2012 | Place / Finish Deck | 0 | 0 | 26-Mar-14 A | | |
| P26-2020 | Place Conc @ Core | 0 | 0 | 26-Mar-14 A | | |
| L08-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 26-Mar-14 A | 28-Mar-14 A | |
| L10-2018 | Remove Reshores | 2 | 0 | 26-Mar-14 A | 27-Mar-14 A | |
| P27-2004 | Shore / Form Deck | 3 | 0 | 27-Mar-14 A | 31-Mar-14 A | |
| P27-2000 | Jump/Resteel/Close Core | 4 | 0 | 29-Mar-14 A | 31-Mar-14 A | |
| P27-2006 | MEP Rough In | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2008 | ReSteel / PT Cables | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2010 | Install Edgeform/Embeds | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P26-2014 | Stress Tendons | 1 | 0 | 31-Mar-14 A | 31-Mar-14 A | |
| L09-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 31-Mar-14 A | 02-Apr-14 A | |
| P24-2016 | Strip / ReShore Deck | 3 | 0 | 01-Apr-14 A | 07-Apr-14 A | |
| L11-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 02-Apr-14 A | |
| L12-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 03-Apr-14 A | |
| P27-2012 | Place / Finish Deck | 0 | 0 | 02-Apr-14 A | | |
| P27-2020 | Place Conc @ Core | 0 | 0 | 02-Apr-14 A | | |
| P28-2002 | FRP Columns Below | 5 | 0 | 02-Apr-14 A | 04-Apr-14 A | |
| P28-2004 | Shore / Form Deck | 4 | 0 | 03-Apr-14 A | 08-Apr-14 A | |

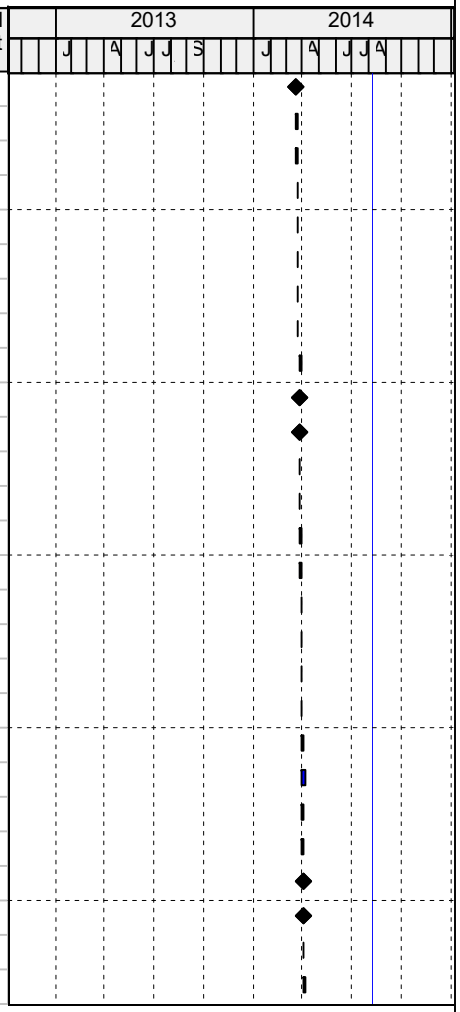


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| P27-2014 | Stress Tendons | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| P25-2016 | Strip / ReShore Deck | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L14-2018 | Remove Reshores | 2 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| P28-2000 | Jump/Resteel/Close Core | 7 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| P28-2006 | MEP Rough In | 4 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2008 | ReSteel / PT Cables | 4 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Apr-14 A | 11-Apr-14 A | |
| L12-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| P28-2012 | Place / Finish Deck | 0 | 0 | 14-Apr-14 A | | |
| P28-2020 | Place Conc @ Core | 0 | 0 | 14-Apr-14 A | | |
| P29-2002 | FRP Columns Above Roof Deck | 3 | 0 | 14-Apr-14 A | 18-Apr-14 A | |
| P26-2016 | Strip / ReShore Deck | 3 | 0 | 14-Apr-14 A | 17-Apr-14 A | |
| L14-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-Apr-14 A | 18-Apr-14 A | |
| P28-2014 | Stress Tendons | 1 | 0 | 17-Apr-14 A | 17-Apr-14 A | |
| P29-2000 | Strip Core | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| P27-2016 | Strip / ReShore Deck | 3 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L15-2018 | Remove Reshores | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| P28-2016 | Strip / ReShore Deck | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L15-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L16-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-May-14 A | 19-May-14 A | |
| L16-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2019 | Grind Ceiling for Skim Coat | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| **Ballroom Catwalk & Roof** | | | | | | |
| PC-2100 | Erect Structural Steel @ Porte Cochere | 3 | 0 | 30-Jan-14 A | 03-Feb-14 A | |

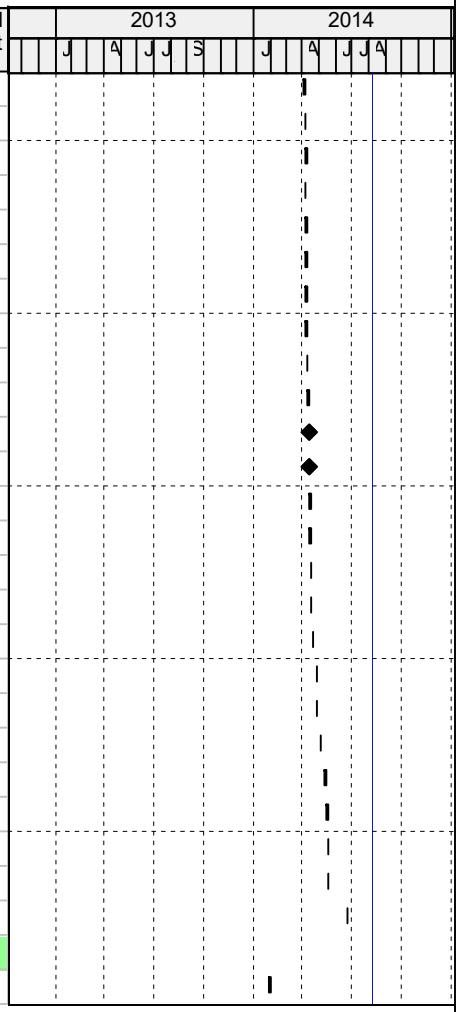



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 7 | 0 | 07-Feb-14 A | 17-Feb-14 A | |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| PC-2102 | Metal Decking @ Porte Cochere/ Roof | 2 | 0 | 17-Apr-14 A | 18-Apr-14 A | |
| BR-2112 | BR - Fireproofing @ Structural Steel | 2 | 0 | 27-May-14 A | 30-May-14 A | |
| Upper Tower - (Levels 3 thru PH) | | | | | | |
| **Mech Penthouse** | | | | | | |
| PH-8706 | Set Mech Equipment @ Tower Roof | 3 | 0 | 22-May-14 A | 28-May-14 A | |
| PH-8708 | Set Equipment @ Penthouse | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| PH-8700 | PH - Structural Steel and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| **Vertical Circulation** | | | | | | |
| Stairs | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 25-Nov-13 A | 26-Nov-13 A | |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 27-Nov-13 A | 03-Dec-13 A | |
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 04-Dec-13 A | 05-Dec-13 A | |
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 06-Dec-13 A | 09-Dec-13 A | |
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 2 | 0 | 03-Feb-14 A | 04-Feb-14 A | |
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 2 | 0 | 06-Feb-14 A | 07-Feb-14 A | |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 2 | 0 | 07-Feb-14 A | 07-Feb-14 A | |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 2 | 0 | 07-Feb-14 A | 10-Feb-14 A | |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 2 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 2 | 0 | 06-Mar-14 A | 07-Mar-14 A | |
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 2 | 0 | 07-Mar-14 A | 10-Mar-14 A | |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |

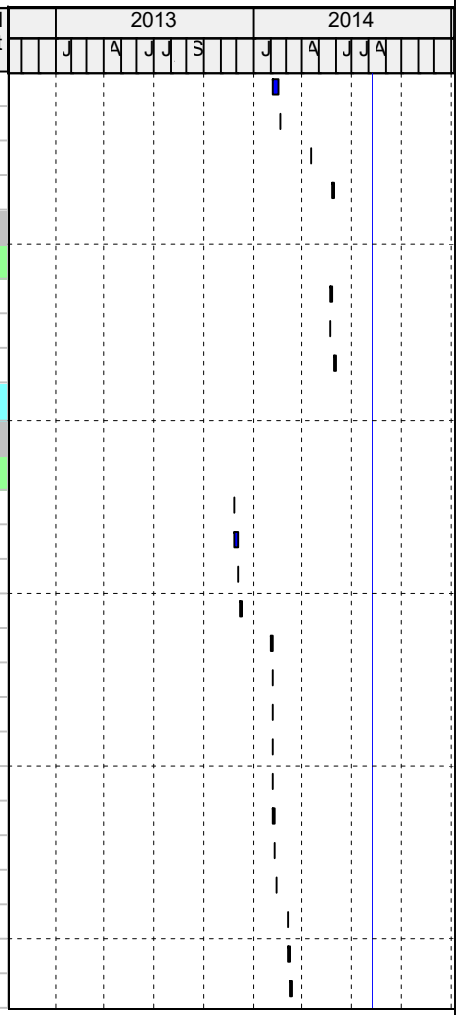



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 2 | 0 | 13-Mar-14 A | 14-Mar-14 A | |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 2 | 0 | 08-Apr-14 A | 21-Apr-14 A | |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| S1-4040 | Stair 1 - Set Mtl Stairs / Railings L18 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 10-Dec-13 A | 11-Dec-13 A | |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 12-Dec-13 A | 13-Dec-13 A | |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 16-Dec-13 A | 17-Dec-13 A | |
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 18-Dec-13 A | 19-Dec-13 A | |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 2 | 0 | 12-Feb-14 A | 13-Feb-14 A | |
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 2 | 0 | 13-Feb-14 A | 13-Feb-14 A | |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 2 | 0 | 13-Feb-14 A | 14-Feb-14 A | |
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 2 | 0 | 19-Feb-14 A | 20-Feb-14 A | |
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 2 | 0 | 21-Feb-14 A | 24-Feb-14 A | |
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 2 | 0 | 19-Mar-14 A | 20-Mar-14 A | |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 2 | 0 | 21-Mar-14 A | 22-Mar-14 A | |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 2 | 0 | 14-May-14 A | 15-May-14 A | |
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 2 | 0 | 16-May-14 A | 19-May-14 A | |
| S2-4038 | Stair 2 - Set Mtl Stairs / Railings L17 | 2 | 0 | 19-May-14 A | 20-May-14 A | |

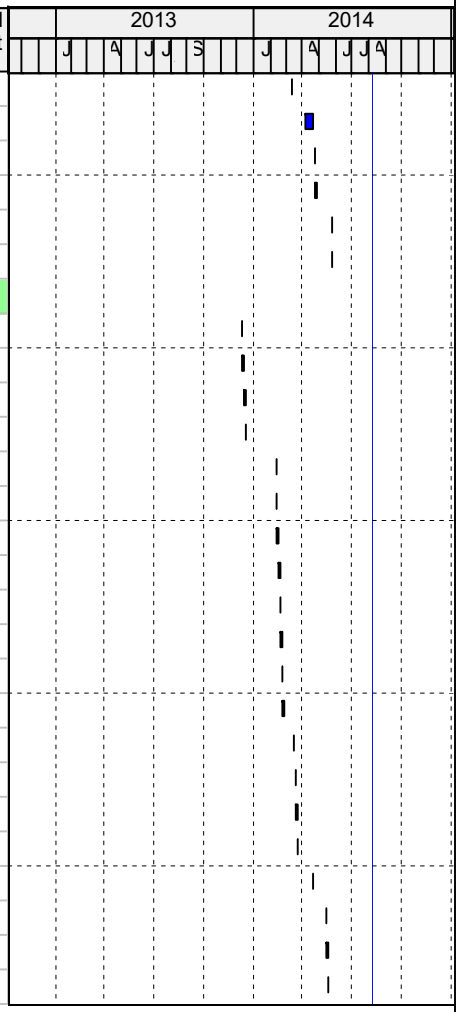



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - Set Metal Stairs / Railings LL2 | 6 | 0 | 05-Mar-14 A | 20-Mar-14 A | |
| S3-4002 | Stair 3 - Set Metal Stairs / Railings LL1 | 6 | 0 | 17-Mar-14 A | 21-Mar-14 A | |
| S3-4004 | Stair 3 - Permanent Railings / Final Finishes | 4 | 4 | 08-Aug-14 | 13-Aug-14 | 84 |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |
| S4-4000 | Stair 4 - Set Metal Stairs / Railings LL2 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4002 | Stair 4 - Set Metal Stairs / Railings LL1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4004 | Stair 4 -Set Metal Stairs / Railings L1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4006 | Stair 4 - Permanent Railings / Final Finishes | 4 | 4 | 08-Aug-14 | 13-Aug-14 | 84 |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |
| S6-4000 | Stair 6 - Set Metal Stairs / Railings | 5 | 0 | 25-Jun-14 A | 01-Jul-14 A | |
| S6-4002 | Stair 6 - Permanent Railings / Final Finishes | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 86 |
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 4 | 08-Aug-14 | 13-Aug-14 | 89 |
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 83 |
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a -Set Metal Stairs / Railings L1 | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 81 |
| S4a-4002 | Stair 4a - Permanent Railings / Final Finishes | 2 | 2 | 15-Aug-14 | 18-Aug-14 | 81 |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 07-Jun-13 A | | |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 0 | 17-Jun-13 A | 21-Jun-13 A | |
| EL-1004 | Elev - Submittal Approval | 21 | 0 | 21-Jun-13 A | 01-Jan-14 A | |
| EL-1006 | Elev - Release to Manufacturing | 14 | 0 | 02-Jan-14 A | 15-Jan-14 A | |
| EL-1008 | Elev - Fabrication (Engineered Geared) | 95 | 0 | 16-Jan-14 A | 14-Jun-14 A | |
| EL-1010 | Elev - Machines delivered | 1 | 0 | 12-May-14 A | 12-May-14 A | |

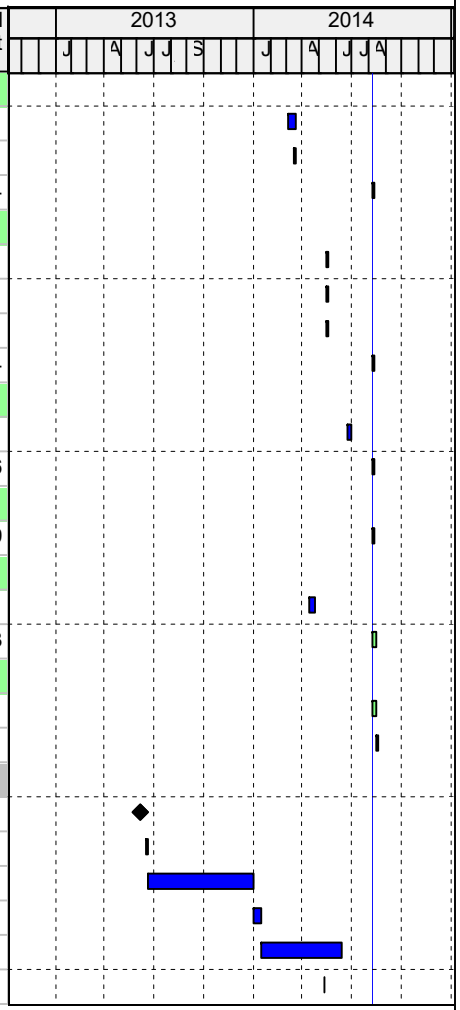



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-1011 | Elev - Elevator Machines Flown & Set At Top Of Hoist | 5 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5016 | Elev 5 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-1216 | Elev 1&2 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-3416 | Elev 3&4 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-1202 | Elev 1&2 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-3402 | Elev 3&4 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-5018 | Elev 5 - Set Hoistway Machines | 3 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| EL-1218 | Elev 1&2 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-3418 | Elev 3&4 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-1200 | Elev 1&2 - Hoistway Clear & Ready (GC) | 0 | 0 | 20-Jun-14 A | | |
| EL-1204 | Elev 1&2 - Install Rails & Brackets | 17 | 0 | 23-Jun-14 A | 15-Jul-14 A | |
| EL-3400 | Elev 3&4 - Hoistway Clear & Ready (GC) | 0 | 0 | 23-Jun-14 A | | |
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 24-Jun-14 A | | |
| EL-1206 | Elev 1&2 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Jul-14 A | |
| EL-1207 | Elev 1&2 - Install Pit Equipment/Car Sling/CWT Fram | 3 | 0 | 15-Jul-14 A | 01-Aug-14 A | |
| EL-1208 | Elev 1&2 - Install MHoist & Cable | 5 | 0 | 16-Jul-14 A | 24-Jul-14 A | |
| EL-3407 | Elev 3&4 - Install Pit Equipment/Car Sling/CWT Fram | 5 | 0 | 16-Jul-14 A | 06-Aug-14 A | |
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 21-Jul-14 A | | |
| EL-5004 | Elev 5 - Install Rails & Brackets | 13 | 2 | 21-Jul-14 A | 11-Aug-14 | 16 |
| EL-3404 | Elev 3&4 - Install Rails & Brackets | 18 | 0 | 23-Jul-14 A | 04-Aug-14 A | |
| EL-3406 | Elev 3&4 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 28-Jul-14 A | |
| EL-3408 | Elev 3&4 - Install Hoist & Cable | 5 | 4 | 07-Aug-14 A | 13-Aug-14 | 15 |
| EL-5006 | Elev 5 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 11-Aug-14 | 16 |
| EL-5007 | Elev 5 - Install Pit Equipment/Car Sling/CWT Frame/V | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 16 |
| EL-1210 | Elev 1&2 - Install Entrances/Doors/Fixtures/Fascia | 19 | 19 | 13-Aug-14 | 09-Sep-14 | 13 |

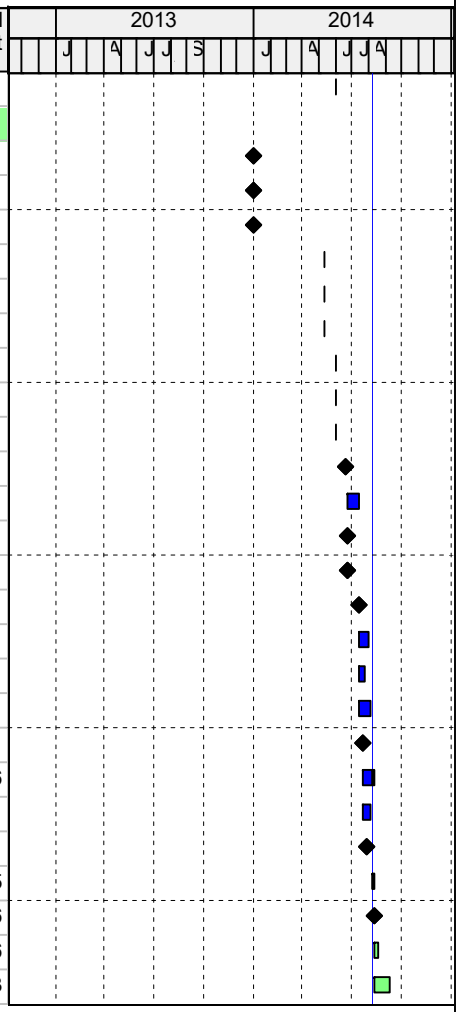


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-3410 | Elev 3&4 - Install Entrances/Doors/Fixtures/Fascia | 30 | 30 | 13-Aug-14 | 24-Sep-14 | 13 |
| EL-5008 | Elev 5 - Install MHoist & Cable | 4 | 4 | 19-Aug-14 | 22-Aug-14 | 16 |
| EL-5010 | Elev 5 - Install Entrances/Doors/Fixtures/Fascia | 21 | 21 | 25-Aug-14 | 23-Sep-14 | 16 |
| EL-1212 | Elev 1&2 - Install Hoistway Equipment/Pipe & Wire | 17 | 17 | 10-Sep-14 | 02-Oct-14 | 23 |
| EL-5012 | Elev 5 - Install Hoistway Equipment/Pipe & Wire | 14 | 14 | 24-Sep-14 | 13-Oct-14 | 16 |
| EL-3412 | Elev 3&4 - Install Hoistway Equipment/Pipe & Wire | 23 | 23 | 25-Sep-14 | 27-Oct-14 | 13 |
| EL-1214 | Elev 1&2 - Install Cab/Wiring/Door Operator(s) | 16 | 16 | 03-Oct-14 | 24-Oct-14 | 23 |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 2 | 2 | 13-Oct-14* | 14-Oct-14 | 10 |
| EL-5014 | Elev 5 - Install Cab/Wiring/Door Operator(s) | 7 | 7 | 14-Oct-14 | 22-Oct-14 | 16 |
| EL-6018 | Elev 6 - Set Hoistway Machines | 2 | 2 | 15-Oct-14 | 16-Oct-14 | 10 |
| EL-6016 | Elev 6 - Hoistway Walls Complete (GC) | 0 | 0 | | 16-Oct-14 | 10 |
| EL-6004 | Elev 6 - Install Cylinders/Rails & Brackets | 4 | 4 | 17-Oct-14 | 22-Oct-14 | 10 |
| EL-6006 | Elev 6 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 22-Oct-14 | 10 |
| EL-5022 | Elev 5 - Adjust | 5 | 5 | 23-Oct-14 | 29-Oct-14 | 16 |
| EL-6007 | Elev 6 - Install Pit Equipment/Car Sling | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 10 |
| EL-1222 | Elev 1&2 - Adjust | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 23 |
| EL-3414 | Elev 3&4 - Install Cab/Wiring/Door Operator(s) | 10 | 10 | 28-Oct-14 | 11-Nov-14 | 13 |
| EL-6010 | Elev 6 - Install Entrances/Doors/Fixtures/Fascia | 3 | 3 | 28-Oct-14 | 30-Oct-14 | 10 |
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 3 | 3 | 30-Oct-14 | 03-Nov-14 | 16 |
| EL-6012 | Elev 6 - Install Hoistway Equipment/Pipe & Wire | 2 | 2 | 31-Oct-14 | 03-Nov-14 | 10 |
| EL-1224 | Elev 1&2 - Clean / Paint / Punchlist | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 23 |
| EL-5026 | Elev 5 - Inspections | 2 | 2 | 04-Nov-14 | 05-Nov-14 | 25 |
| EL-6014 | Elev 6 - Install Cab/Wiring/Door Operator(s) | 5 | 5 | 04-Nov-14 | 11-Nov-14 | 10 |
| EL-1226 | Elev 1&2 - Inspections | 2 | 2 | 06-Nov-14 | 07-Nov-14 | 36 |
| EL-3422 | Elev 3&4 - Adjust | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 13 |
| EL-6022 | Elev 6 - Adjust | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 10 |
| EL-3424 | Elev 3&4 - Clean / Paint / Punchlist | 3 | 3 | 19-Nov-14 | 21-Nov-14 | 13 |

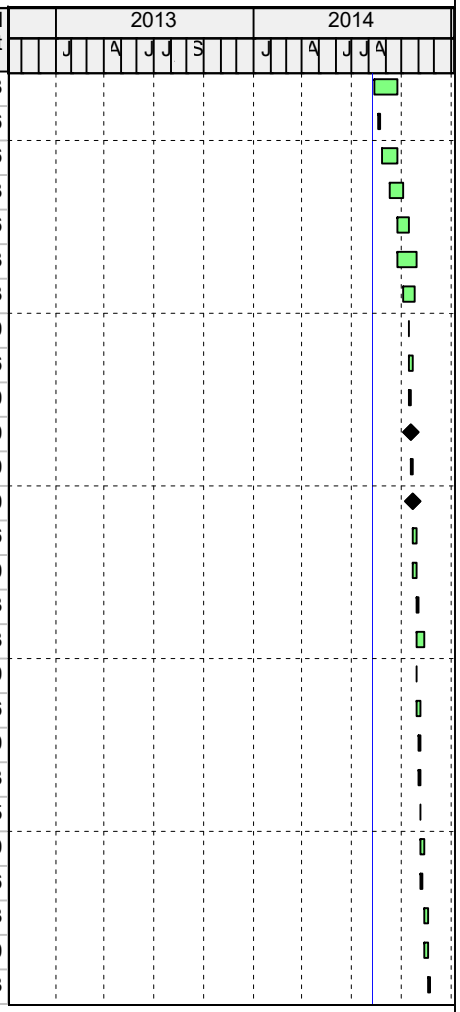



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6024 | Elev 6 - Clean / Paint / Punchlist | 1 | 1 | 19-Nov-14 | 19-Nov-14 | 10 |
| EL-6026 | Elev 6 - Inspections | 1 | 1 | 20-Nov-14 | 20-Nov-14 | 18 |
| EL-3426 | Elev 3&4 - Inspections | 2 | 2 | 22-Nov-14 | 23-Nov-14 | 22 |
| **Exterior Shell** | | | | | | |
| **Elevations** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2** | | | | | | |
| L3D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Feb-14 A | 12-Feb-14 A | |
| L3-5308 | L3- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 17-Feb-14 A | 21-Feb-14 A | |
| L4D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Feb-14 A | 19-Feb-14 A | |
| L4-5308 | L4- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Feb-14 A | 28-Feb-14 A | |
| L5D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Feb-14 A | 26-Feb-14 A | |
| L5-5308 | L5- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 03-Mar-14 A | 07-Mar-14 A | |
| L6D5308 | Deliver/Stock Wall Panels | 1 | 0 | 05-Mar-14 A | 05-Mar-14 A | |
| L6-5308 | L6- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L7-5308 | L7- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L7D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Mar-14 A | 12-Mar-14 A | |
| L8D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Mar-14 A | 19-Mar-14 A | |
| L8-5308 | L8- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Mar-14 A | 28-Mar-14 A | |
| L9D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L9-5308 | L9- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 31-Mar-14 A | 07-Apr-14 A | |
| 10D5308 | Deliver/Stock Wall Panels | 1 | 0 | 02-Apr-14 A | 02-Apr-14 A | |
| L10-5308 | L10- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 07-Apr-14 A | 11-Apr-14 A | |
| 11D5308 | Deliver/Stock Wall Panels | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L11-5308 | L11- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 11-Apr-14 A | 18-Apr-14 A | |
| 12D5308 | Deliver/Stock Wall Panels | 1 | 0 | 16-Apr-14 A | 16-Apr-14 A | |
| L12-5308 | L12- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Apr-14 A | 25-Apr-14 A | |

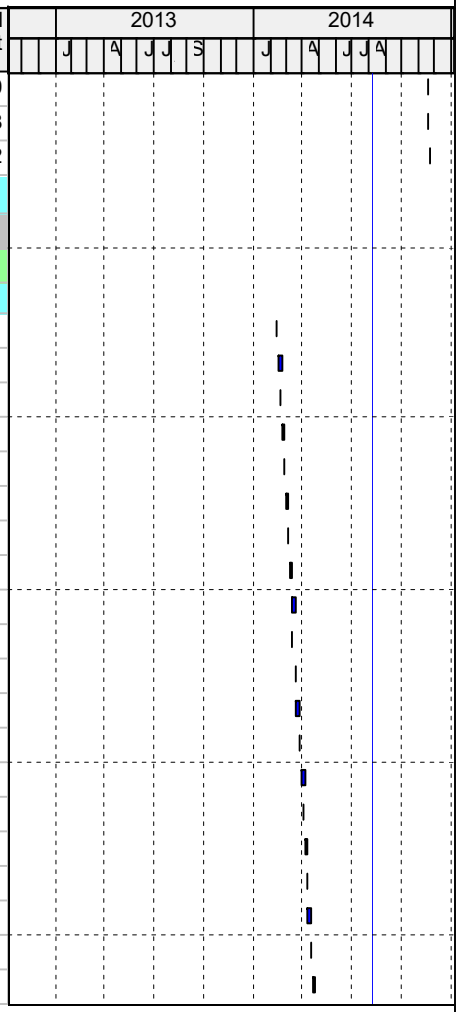



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| 14D5308 | Deliver/Stock Wall Panels | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L14-5308 | L14 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Apr-14 A | 01-May-14 A | |
| 15D5308 | Deliver/Stock Wall Panels | 1 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L15-5308 | L15 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| 16D5308 | Deliver/Stock Wall Panels | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L16-5308 | L16- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| 17D5308 | Deliver/Stock Wall Panels | 1 | 0 | 14-May-14 A | 14-May-14 A | |
| L17-5308 | L17 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 20-May-14 A | 11-Jun-14 A | |
| LL2-5308 | LL2 Thru L4 - Support Frame/Sheathing for Metal Wa | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL1-5308 | LL1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| L1-5308 | L1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| **Level 1** | | | | | | |
| EP-5110 | L1 - Revolving Doors | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 0 |
| L1-5102 | L1 - Storefront Frames | 8 | 8 | 25-Aug-14 | 04-Sep-14 | 0 |
| L1-5104 | L1 - Storefront Glazing | 6 | 6 | 03-Sep-14 | 10-Sep-14 | 0 |
| L3-5102 | L3- Storefront Frames | 7 | 7 | 11-Sep-14 | 19-Sep-14 | 13 |
| L3-5104 | L3 - Storefront Glazing | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 13 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Levels 3-4** | | | | | | |
| L3-5130 | L3 - Install Punch Windows | 5 | 0 | 24-Feb-14 A | 10-Mar-14 A | |
| L4-5130 | L4 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 12-Mar-14 A | |
| L5-5130 | L5 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L6-5130 | L6- Install Punch Windows | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L7-5130 | L7 - Install Punch Windows | 5 | 0 | 18-Mar-14 A | 21-Mar-14 A | |
| L8-5130 | L8 - Install Punch Windows | 5 | 0 | 24-Mar-14 A | 28-Mar-14 A | |
| L9-5130 | L9 - Install Punch Windows | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L10-5130 | L10 - Install Punch Windows | 5 | 0 | 08-Apr-14 A | 11-Apr-14 A | |

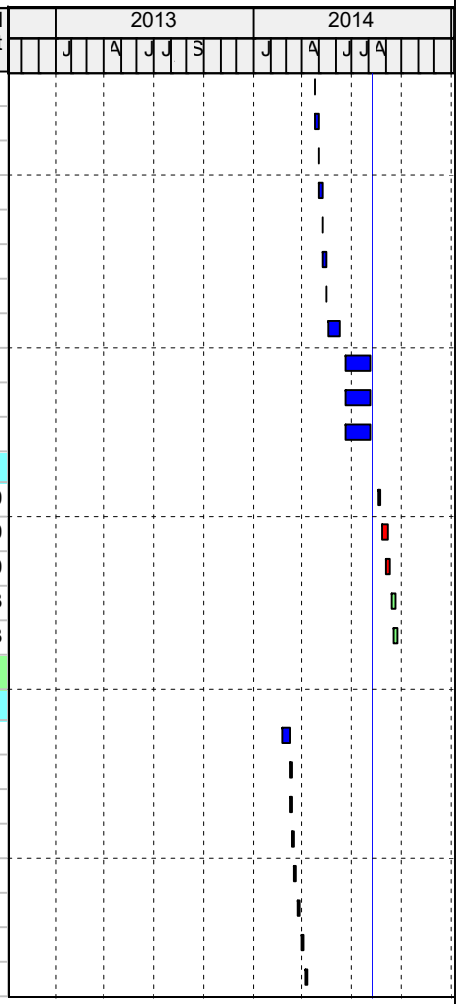


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-5130 | L11 - Install Punch Windows | 5 | 0 | 14-Apr-14 A | 21-Apr-14 A | |
| L12-5130 | L12 - Install Punch Windows | 5 | 0 | 22-Apr-14 A | 25-Apr-14 A | |
| L14-5130 | L14 - Install Punch Windows | 5 | 0 | 28-Apr-14 A | 05-May-14 A | |
| L15-5130 | L15 - Install Punch Windows | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| L16-5130 | L16 - Install Punch Windows | 5 | 0 | 12-May-14 A | 20-May-14 A | |
| L17-5130 | L17 - Install Punch Windows | 5 | 0 | 27-May-14 A | 16-Jun-14 A | |
| Roofs | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 13 |
| RF-4026 | L1 - City Park - Protection Board | 3 | 3 | 18-Sep-14 | 22-Sep-14 | 13 |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 13 |
| **Pool Membrane - (elev 18')** | | | | | | |
| RF-4034 | Pool - Install plumbing | 3 | 3 | 18-Aug-14* | 20-Aug-14 | 13 |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |
| RF-4010 | AR - Set Mechanical Equipment | 5 | 0 | 10-Jun-14 A | 12-Jun-14 A | |
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 10 | 7 | 04-Aug-14 A | 15-Aug-14 | 20 |
| RF-4012 | AR - Coping / Flashing | 4 | 4 | 18-Aug-14 | 21-Aug-14 | 83 |
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 8 | 8 | 29-Aug-14 | 10-Sep-14 | 13 |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |
| PC-4008 | RF - Entry / Porte Cochere Roofing System | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 17 |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | RF - Upper Ballroom Roofing System | 3 | 0 | 28-Jul-14 A | 31-Jul-14 A | |
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 4 | 0 | 31-Jul-14 A | 04-Aug-14 A | |
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |
| RF-4018 | TR - Terrace Roof - Green Roofing System | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 50 |

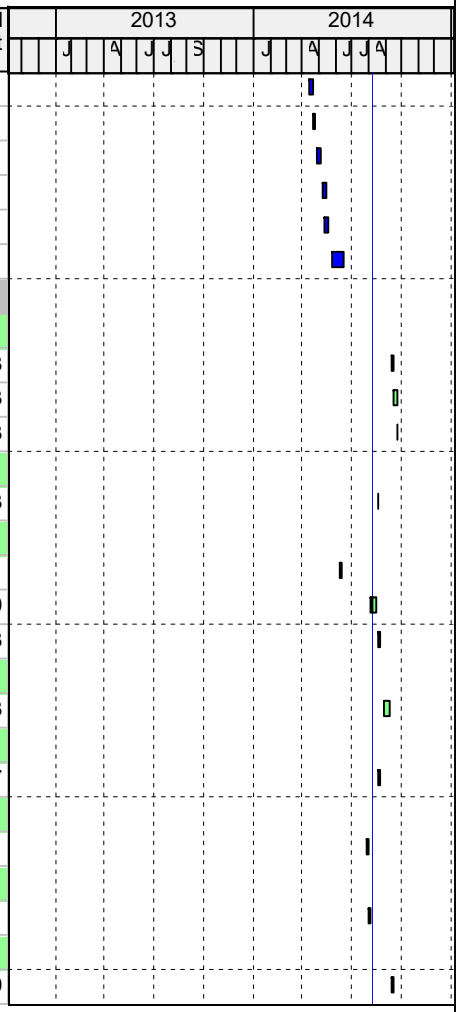


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| RF-4020 | TR - Terrace Roof - Coping / Flashing | 3 | 3 | 18-Sep-14 | 22-Sep-14 | 50 |
| RF-4022 | TR - Terrace Roof - Glass Railing | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 50 |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Perimeter Framing / Sul | 10 | 0 | 02-Jun-14 A | 08-Jul-14 A | |
| RF-4002 | Tower Roof - Roofing System | 10 | 9 | 06-Aug-14 A | 18-Aug-14 | 20 |
| **PH - Roof - (elev 173')** | | | | | | |
| RF-4030 | PH - Roofing System | 2 | 1 | 06-Aug-14 A | 08-Aug-14 | 20 |
| RF-4032 | PH - Coping / Flashing | 3 | 3 | 11-Aug-14 | 13-Aug-14 | 87 |
| **Rough-In's** | | | | | | |
| Lower Podium - (Levels LL2 / LL1 / 1 / 2) | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6002 | LL4 - Layout | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| LL4-6008 | LL4 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL4-6012 | LL4 - Fire Sprinkler Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6014 | LL4 - Plumbing Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6018 | LL4 - HVAC Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6004 | LL4 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL4-6016 | LL4 - Electrical Rl | 10 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties Rl | 8 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6010 | LL4 - Elevator pits | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| LL4-6020 | LL4 - H Mtl Frames | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL4-6024 | LL4 - Inspections | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 58 |
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6002 | LL3 - Layout | 1 | 0 | 19-Nov-13 A | 19-Nov-13 A | |
| LL3-6008 | LL3 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL3-6012 | LL3 - Fire Sprinkler Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |

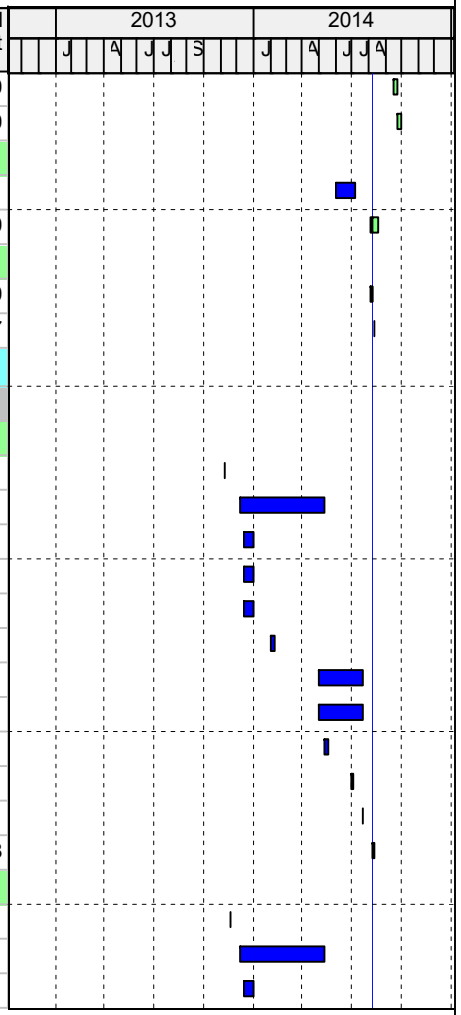



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-6014 | LL3 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6018 | LL3 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6004 | LL3 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL3-6020 | LL3 - H Mtl Frames | 3 | 0 | 08-May-14 A | 09-May-14 A | |
| LL3-6010 | LL3 - F/P Curbs | 5 | 0 | 19-May-14 A | 19-May-14 A | |
| LL3-6016 | LL3 - Electrical RI | 2 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties RI | 8 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL3-6024 | LL3 - Inspections | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 53 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6002 | LL2 - Layout | 1 | 0 | 14-Jan-14 A | 14-Jan-14 A | |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| LL2-6012 | LL2 - Fire Sprinkler RI | 10 | 0 | 21-Jan-14 A | 03-Feb-14 A | |
| LL2-6014 | LL2 - Plumbing RI | 10 | 0 | 21-Jan-14 A | 14-Feb-14 A | |
| LL2E-6016 | LL2 - Electrical RI | 8 | 0 | 03-Feb-14 A | 17-Mar-14 A | |
| LL2-6016 | LL2 - Electrical RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2-6018 | LL2 - HVAC RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2–6004 | LL2 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL2E-6004 | LL2 - CMU Walls | 10 | 0 | 04-Mar-14 A | 09-May-14 A | |
| LL2E-6012 | LL2 - Fire Sprinkler RI | 8 | 0 | 21-Mar-14 A | 01-Apr-14 A | |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 24-Apr-14 A | |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 3 | 0 | 23-Apr-14 A | 21-Jul-14 A | |
| LL2E-6020 | LL2 - H Mtl Frames | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| LL2-6020 | LL2 - H Mtl Frames | 3 | 0 | 12-May-14 A | 13-May-14 A | |
| LL2E-6008 | LL2 - Int Wall Framing | 5 | 0 | 13-May-14 A | 22-Jun-14 A | |
| LL2E-6014 | LL2 - Plumbing RI | 8 | 0 | 13-May-14 A | 30-May-14 A | |
| LL2E-6018 | LL2 - HVAC RI | 8 | 0 | 13-May-14 A | 04-Aug-14 A | |

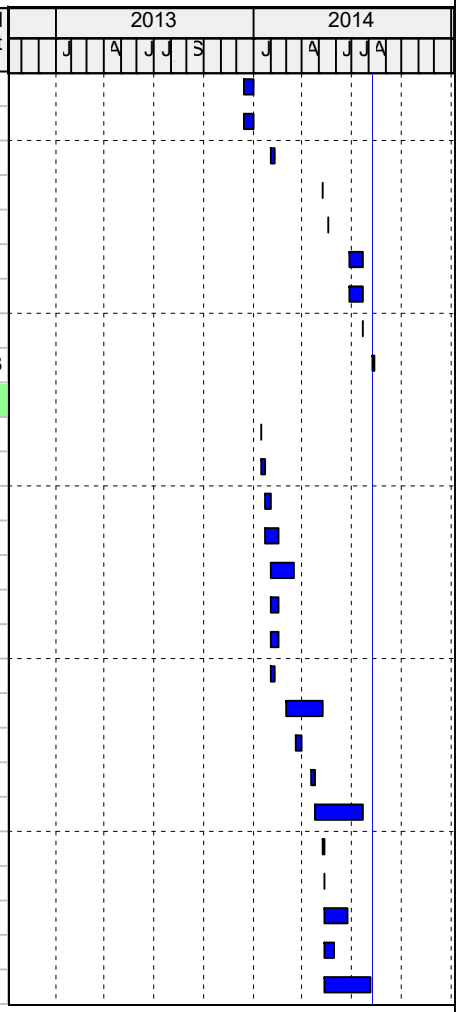



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2E-6022 | LL2 - Fire Alarm / Elec Specialties RI (East of 10) | 8 | 2 | 13-May-14 A | 11-Aug-14 | 39 |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties RI (West of 10) | 8 | 2 | 19-May-14 A | 11-Aug-14 | 29 |
| LL2-6015 | LL2 - Main Elect Room Set Equip / RI - Power to Ma | 15 | 2 | 30-Jun-14 A | 11-Aug-14 | 76 |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 0 | 16-Jul-14 A | 21-Jul-14 A | |
| LL2-6024 | LL2 - Inspections | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 29 |
| LL2-6010 | LL2 - F/P Curbs @ Parking | 3 | 3 | 08-Sep-14 | 10-Sep-14 | 56 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6002 | Layout | 3 | 0 | 03-Jan-14 A | 08-Jan-14 A | |
| LL1-6008 | Int Wall Framing & Inspection | 6 | 0 | 08-Jan-14 A | 21-Jul-14 A | |
| LL1-Z2-6002 | Layout | 3 | 0 | 08-Jan-14 A | 14-Jan-14 A | |
| LL1-Z3-6002 | Layout | 3 | 0 | 14-Jan-14 A | 17-Jan-14 A | |
| LL1-Z2-6008 | Int Wall Framing & Inspection | 6 | 0 | 17-Jan-14 A | 01-Aug-14 A | |
| LL1-Z3-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-Jan-14 A | 04-Aug-14 A | |
| LL1-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 09-May-14 A | |
| LL1-Z2-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 28-Apr-14 A | |
| LL1-Z3-6004 | CMU Walls (At All Areas North of Q-Line) | 3 | 0 | 03-Feb-14 A | 13-May-14 A | |
| LL1C-6012 | Complete Fire Sprinkler RI @ Ceilings | 10 | 2 | 17-Feb-14 A | 12-Aug-14 | 31 |
| LL1C-6016 | Complete Electrical RI @ Ceilings | 10 | 2 | 17-Feb-14 A | 12-Aug-14 | 31 |
| LL1C-6018 | Complete HVAC RI @ Ceilings | 10 | 3 | 17-Feb-14 A | 13-Aug-14 | 30 |
| LL1C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 10 | 2 | 17-Feb-14 A | 12-Aug-14 | 31 |
| LL1-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 30-Apr-14 A | |
| LL1-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-Z2-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |

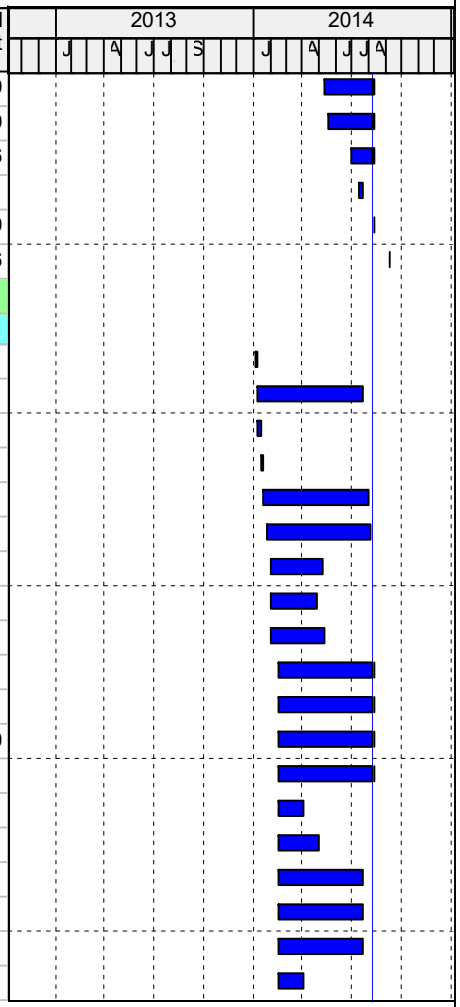



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6018 | HVAC RI | 20 | 6 | 17-Feb-14 A | 15-Aug-14 | 28 |
| LL1-Z2-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z3-6012 | Fire Sprinkler RI (At All Areas North of Q-Line) | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z3-6014 | Plumbing RI | 20 | 1 | 17-Feb-14 A | 08-Aug-14 | 97 |
| LL1-Z3-6016 | Electrical RI | 20 | 1 | 17-Feb-14 A | 08-Aug-14 | 30 |
| LL1-Z3-6018 | HVAC RI | 20 | 6 | 17-Feb-14 A | 15-Aug-14 | 92 |
| LL1-Z3-6022 | Fire Alarm / Elec Specialties RI | 20 | 1 | 17-Feb-14 A | 08-Aug-14 | 30 |
| LL1-Z2C-6012 | Complete Fire Sprinkler RI @ Ceilings | 15 | 5 | 24-Feb-14 A | 21-Aug-14 | 24 |
| LL1-Z2C-6014 | Complete Plumbing RI @ Ceilings | 15 | 5 | 24-Feb-14 A | 21-Aug-14 | 24 |
| LL1-Z2C-6016 | Complete Electrical RI @ Ceilings | 15 | 5 | 24-Feb-14 A | 21-Aug-14 | 24 |
| LL1-Z2C-6018 | Complete HVAC RI @ Ceilings | 15 | 5 | 24-Feb-14 A | 21-Aug-14 | 24 |
| LL1-Z2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 15 | 5 | 24-Feb-14 A | 21-Aug-14 | 24 |
| LL1-Z2-6020 | Hollow Metal Door Frames | 5 | 0 | 17-Mar-14 A | 04-Apr-14 A | |
| LL1-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| LL1-Z3-6020 | Hollow Metal Door Frames (At All Areas North of Q-Lir | 1 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| L1B-6004 | CMU Walls [including East Service Corridor] | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L1L-6002 | Layout [including back of house] | 3 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 29-Apr-14 A | |
| L1B-6008 | Int Wall Framing & Inspection | 6 | 4 | 21-Apr-14 A | 13-Aug-14 | 0 |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 5 | 0 | 25-Apr-14 A | 21-Jul-14 A | |
| LL1C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L1K-6004 | CMU Walls [including public restroom] | 3 | 0 | 05-May-14 A | 08-May-14 A | |
| L1K-6002 | Layout [including public restroom] | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| L1K-6008 | Int Wall Framing & Inspection | 4 | 11 | 09-May-14 A | 22-Aug-14 | 11 |
| L1B-6002 | Layout [including East Service Corridor] | 3 | 0 | 14-May-14 A | 27-May-14 A | |

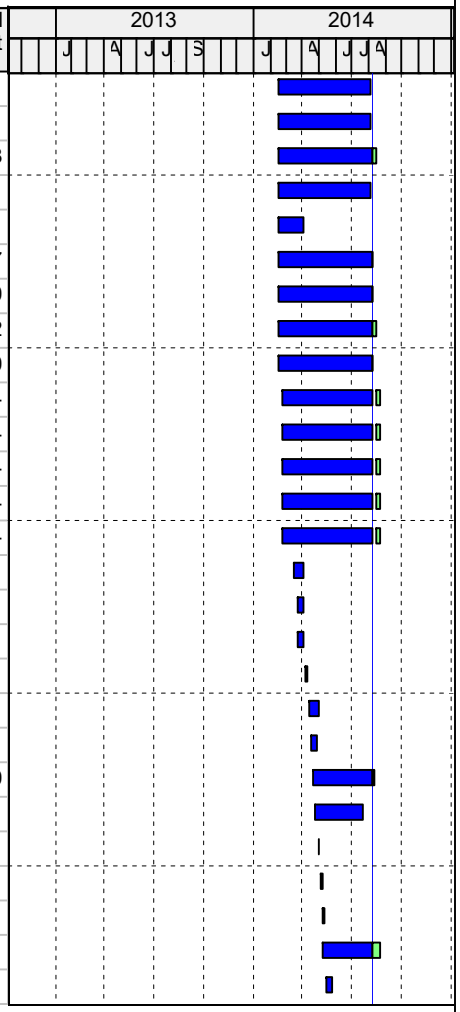


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-6008 | Int Wall Framing & Inspection | 6 | 5 | 27-May-14 A | 27-Aug-14 | 0 |
| L1L-6004 | CMU Walls [including back of house] | 3 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L1K-6012 | Fire Sprinkler RI | 10 | 5 | 02-Jun-14 A | 26-Aug-14 | 11 |
| L1K-6014 | Plumbing RI | 10 | 5 | 02-Jun-14 A | 26-Aug-14 | 11 |
| L1K-6016 | Electrical RI | 10 | 6 | 02-Jun-14 A | 26-Aug-14 | 11 |
| L1K-6018 | HVAC RI | 10 | 5 | 02-Jun-14 A | 26-Aug-14 | 11 |
| L1B-6014 | Plumbing RI [including East Service Corridor] | 10 | 0 | 16-Jun-14 A | 24-Jun-14 A | |
| L1B-6018 | HVAC RI | 10 | 5 | 20-Jun-14 A | 15-Aug-14 | 8 |
| L1B-6012 | Fire Sprinkler RI | 10 | 5 | 21-Jun-14 A | 15-Aug-14 | 8 |
| L1L-6018 | HVAC RI | 5 | 5 | 23-Jun-14 A | 04-Sep-14 | 0 |
| L1L-6014 | Plumbing RI | 5 | 5 | 24-Jun-14 A | 04-Sep-14 | 0 |
| L1L-6010 | CMU Seismic Clips [including back of house] [DELET | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1L-6012 | Fire Sprinkler RI | 5 | 5 | 25-Jun-14 A | 04-Sep-14 | 0 |
| L1L-6016 | Electrical RI | 5 | 5 | 25-Jun-14 A | 04-Sep-14 | 0 |
| L1L-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 27-Jun-14 A | 04-Sep-14 | 0 |
| L1K-6022 | Fire Alarm / Elec Specialties RI | 10 | 5 | 27-Jun-14 A | 26-Aug-14 | 11 |
| LL1-Z3-6009 | Frame Ceilings [DELETED] | 4 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1B-6016 | Electrical RI | 10 | 5 | 07-Jul-14 A | 15-Aug-14 | 8 |
| L1B-6022 | Fire Alarm / Elec Specialties RI | 10 | 5 | 07-Jul-14 A | 15-Aug-14 | 8 |
| LL1-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-Z2-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L1B-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-6024 | Inspections for Cover | 1 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L1B-6020 | Hollow Metal Door Frames | 5 | 4 | 01-Aug-14 A | 13-Aug-14 | 10 |
| LL1-Z3-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L1K-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 06-Aug-14 A | |
| LL1-Z2-6024 | Inspections for Cover | 2 | 1 | 07-Aug-14 A | 08-Aug-14 | 24 |

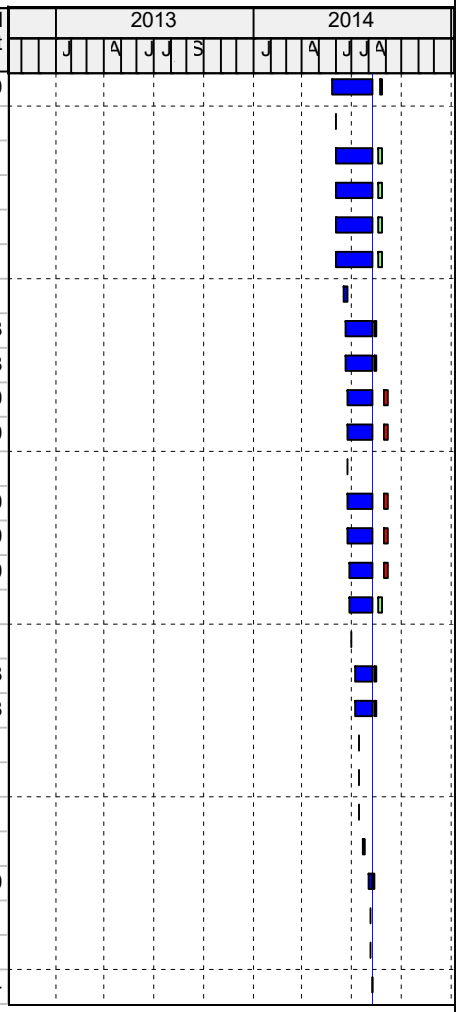



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-6024 | Inspections for Cover | 2 | 2 | 11-Aug-14 | 12-Aug-14 | 30 |
| LL1-6009 | Frame Ceilings & Inspection | 6 | 6 | 14-Aug-14 | 21-Aug-14 | 30 |
| L1B-6024 | Inspections for Cover | 2 | 2 | 18-Aug-14 | 19-Aug-14 | 8 |
| L1K-6020 | Hollow Metal Door Frames | 5 | 5 | 18-Aug-14 | 22-Aug-14 | 13 |
| LL1-Z3C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 30 |
| LL1-Z3C-6014 | Complete Plumbing RI @ Ceilings | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 30 |
| LL1-Z3C-6016 | Complete Electrical RI @ Ceilings | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 30 |
| LL1-Z3C-6018 | Complete HVAC RI @ Ceilings | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 30 |
| LL1-Z3C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 30 |
| L1L-6020 | Hollow Metal Door Frames | 5 | 5 | 21-Aug-14 | 27-Aug-14 | 5 |
| LL1-Z2-6009 | Frame Ceilings & Inspection | 6 | 6 | 22-Aug-14 | 29-Aug-14 | 24 |
| L1K-6024 | Inspections for Cover | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 11 |
| L1K-6009 | Frame Ceilings [public restroom] | 3 | 3 | 02-Sep-14 | 04-Sep-14 | 24 |
| L1L-6024 | Inspections for Cover | 2 | 2 | 05-Sep-14 | 08-Sep-14 | 0 |
| L1BC-6012 | Complete Fire Sprinkler RI @ Ceilings | 7 | 7 | 09-Sep-14 | 17-Sep-14 | 8 |
| L1BC-6014 | Complete Plumbing RI @ Ceilings | 7 | 7 | 09-Sep-14 | 17-Sep-14 | 8 |
| L1BC-6018 | Complete HVAC RI @ Ceilings | 7 | 7 | 09-Sep-14 | 17-Sep-14 | 8 |
| L1B-6009 | Frame Ceilings | 7 | 7 | 17-Sep-14 | 25-Sep-14 | 8 |
| L1BC-6016 | Complete Electrical RI @ Ceilings & Inspection | 7 | 7 | 22-Sep-14 | 30-Sep-14 | 8 |
| L1BC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 7 | 7 | 22-Sep-14 | 30-Sep-14 | 8 |
| L1KC-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 4 | 4 | 24-Sep-14 | 29-Sep-14 | 11 |
| L1KC-6014 | Complete Plumbing RI @ Ceilings & Inspection | 4 | 4 | 24-Sep-14 | 29-Sep-14 | 11 |
| L1KC-6016 | Complete Electrical RI @ Ceilings & Inspection | 4 | 4 | 24-Sep-14 | 29-Sep-14 | 11 |
| L1KC-6018 | Complete HVAC RI @ Ceilings & Inspection | 4 | 4 | 24-Sep-14 | 29-Sep-14 | 11 |
| L1KC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 4 | 4 | 24-Sep-14 | 29-Sep-14 | 11 |
| L1LC-6012 | Complete Fire Sprinkler RI @ Ceilings | 4 | 4 | 25-Sep-14 | 30-Sep-14 | 0 |
| L1LC-6014 | Complete Plumbing RI @ Ceilings | 4 | 4 | 25-Sep-14 | 30-Sep-14 | 0 |

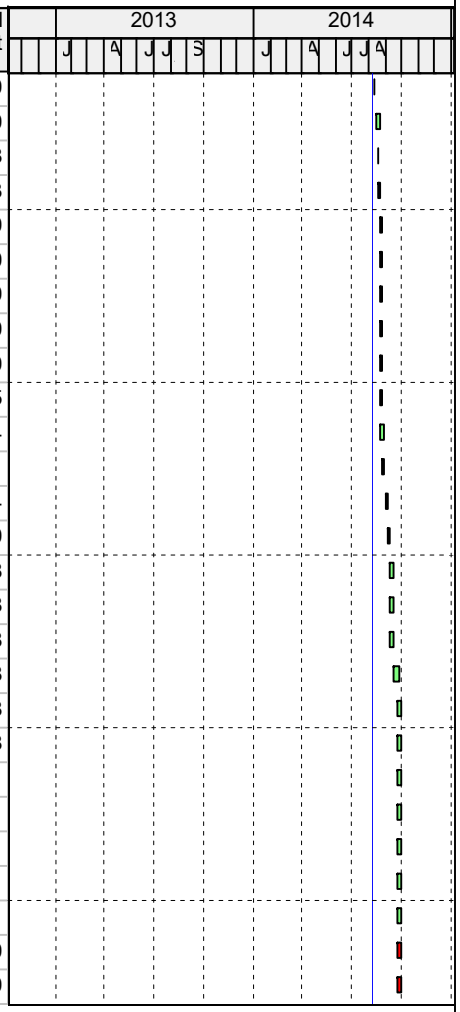


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1LC-6016 | Complete Electrical RI @ Ceilings | 4 | 4 | 25-Sep-14 | 30-Sep-14 | 0 |
| L1LC-6018 | Complete HVAC RI @ Ceilings | 4 | 4 | 25-Sep-14 | 30-Sep-14 | 0 |
| L1LC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 4 | 4 | 25-Sep-14 | 30-Sep-14 | 0 |
| L1L-6009 | Frame Ceilings & Inspection | 13 | 13 | 30-Sep-14 | 16-Oct-14 | 0 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 0 | 17-Apr-14 A | 09-May-14 A | |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6006 | L2 - Support Frame/Sheathing for Metal Panels | 6 | 0 | 23-Apr-14 A | 07-Aug-14 A | |
| L02-6008 | L2 - Int Wall Framing | 10 | 0 | 25-Apr-14 A | 17-Jul-14 A | |
| L02-6014 | L2 - Plumbing RI | 15 | 2 | 28-Apr-14 A | 11-Aug-14 | 33 |
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 0 | 28-Apr-14 A | 09-May-14 A | |
| L02-6004 | L2 - CMU Walls | 5 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L02-6002 | L2 - Layout | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L02-6018 | L2 - HVAC RI (including equipment) | 20 | 3 | 18-Jun-14 A | 12-Aug-14 | 36 |
| L02-6016 | L2 - Electrical RI | 10 | 5 | 24-Jun-14 A | 14-Aug-14 | 33 |
| L02-6022 | L2 - Fire Alarm / Elec Specialties RI | 10 | 7 | 24-Jun-14 A | 18-Aug-14 | 33 |
| L02-6012 | L2 - Fire Sprinkler RI | 10 | 6 | 26-Jun-14 A | 15-Aug-14 | 33 |
| L02-6020 | L2 - H Mtl Frames | 5 | 0 | 11-Jul-14 A | 17-Jul-14 A | |
| L02-6024 | L2 - Inspections | 2 | 2 | 18-Aug-14 | 19-Aug-14 | 33 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L07-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 01-Apr-11 A | 11-Apr-11 A | |
| L04-6012 | Fire Sprinkler Mains | 5 | 0 | 01-Feb-14 A | 03-Apr-14 A | |
| L03-8219 | HVAC Risers | 5 | 0 | 11-Feb-14 A | 23-Mar-14 A | |
| L03-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 11-Feb-14 A | 03-Mar-14 A | |
| L03-6002 | Layout | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |

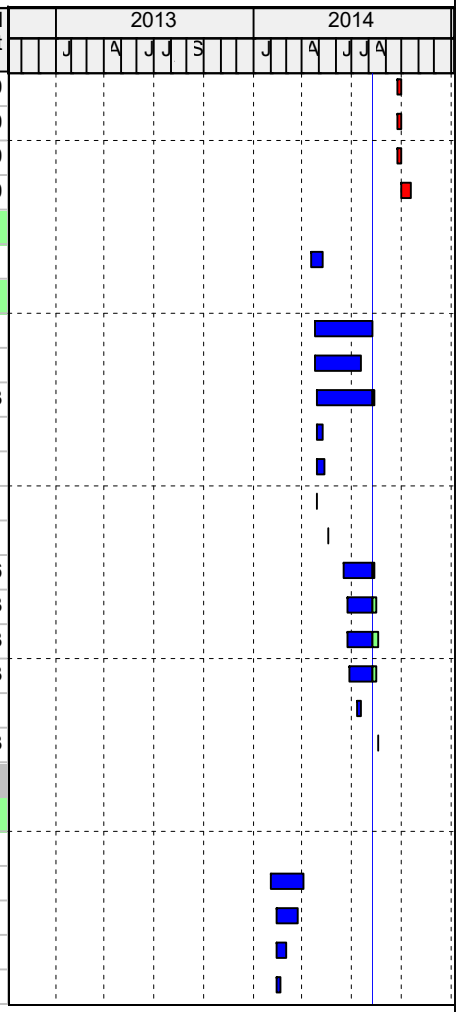



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8219 | HVAC Risers | 5 | 0 | 13-Feb-14 A | 23-Mar-14 A | |
| L05-8219 | HVAC Risers | 5 | 0 | 17-Feb-14 A | 03-Mar-14 A | |
| L03-6008 | Frame Shaft Walls | 3 | 0 | 18-Feb-14 A | 26-Mar-14 A | |
| L04-6002 | Layout | 5 | 0 | 19-Feb-14 A | 25-Feb-14 A | |
| L04-6008 | Frame Shaft Walls | 3 | 0 | 20-Feb-14 A | 26-Mar-14 A | |
| L03-6011 | PreRock Shafts | 2 | 0 | 24-Feb-14 A | 25-Mar-14 A | |
| L03-6010 | Frame Walls | 5 | 0 | 25-Feb-14 A | 25-Mar-14 A | |
| L05-6002 | Layout | 5 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| L04-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 28-Feb-14 A | 05-Mar-14 A | |
| L03-6016 | Electrical RI | 5 | 0 | 03-Mar-14 A | 04-Apr-14 A | |
| L03-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 12-Mar-14 A | |
| L04-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 13-Mar-14 A | |
| L04-6010 | Frame Walls | 5 | 0 | 04-Mar-14 A | 05-Jun-14 A | |
| L05-6008 | Frame Shaft Walls | 3 | 0 | 05-Mar-14 A | 27-Mar-14 A | |
| L06-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L07-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L05-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 06-Mar-14 A | 21-Mar-14 A | |
| L03-6020 | Install Hollow Metal Frames | 3 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L04-6020 | Install Hollow Metal Frames | 3 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L05-6010 | Frame Walls | 5 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L06-6002 | Layout | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L04-6011 | PreRock Shafts | 2 | 0 | 18-Mar-14 A | 25-Mar-14 A | |
| L05-6009 | Inspect Shafts | 1 | 0 | 18-Mar-14 A | 18-Mar-14 A | |
| L05-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| L06-6008 | Frame Shaft Walls | 3 | 0 | 19-Mar-14 A | 03-Apr-14 A | |
| L06-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 27-Mar-14 A | |
| L04-6016 | Electrical RI | 5 | 0 | 20-Mar-14 A | 09-Apr-14 A | |

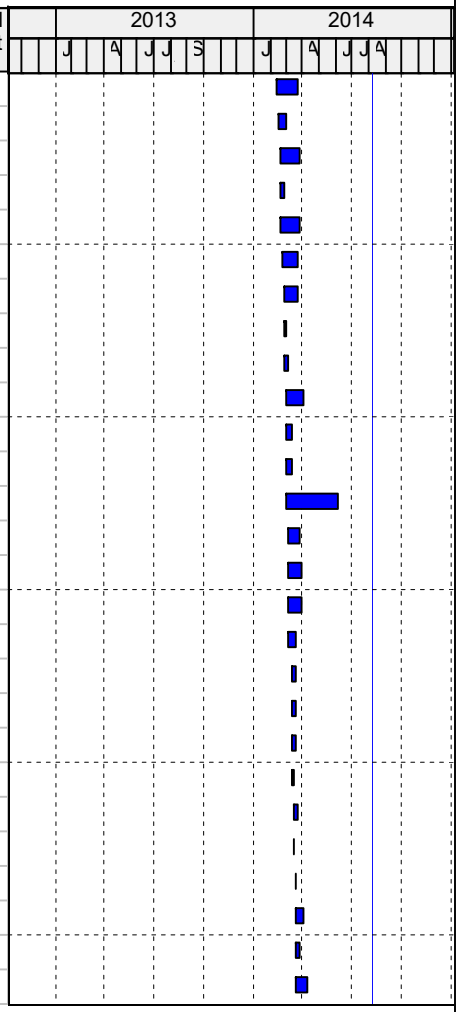



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 26-Mar-14 A | |
| L06-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 07-Apr-14 A | |
| L07-6002 | Layout | 5 | 0 | 24-Mar-14 A | 30-Apr-14 A | |
| L03-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L03-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L05-6016 | Electrical RI | 5 | 0 | 25-Mar-14 A | 05-Jun-14 A | |
| L04-6019 | Complete Top Out GWB | 2 | 0 | 26-Mar-14 A | 06-Jun-14 A | |
| L05-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L06-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| L03-6019 | Complete Top Out GWB | 2 | 0 | 27-Mar-14 A | 02-May-14 A | |
| L08-6002 | Layout | 5 | 0 | 27-Mar-14 A | 02-Apr-14 A | |
| L05-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 28-Mar-14 A | 03-Apr-14 A | |
| L06-6010 | Frame Walls | 5 | 0 | 28-Mar-14 A | 07-Apr-14 A | |
| L03-6012 | Fire Sprinkler Mains | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L07-6008 | Frame Shaft Walls | 3 | 0 | 31-Mar-14 A | 03-Apr-14 A | |
| L05-6019 | Complete Top Out GWB | 2 | 0 | 01-Apr-14 A | 08-Apr-14 A | |
| L08-6008 | Frame Shaft Walls | 3 | 0 | 02-Apr-14 A | 21-Apr-14 A | |
| L03-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L04-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L05-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L06-6016 | Electrical RI | 5 | 0 | 03-Apr-14 A | 15-Apr-14 A | |
| L07-6009 | Inspect Shafts | 1 | 0 | 03-Apr-14 A | 03-Apr-14 A | |
| L07-6011 | PreRock Shafts | 2 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| L05-6012 | Fire Sprinkler Mains | 5 | 0 | 04-Apr-14 A | 30-Apr-14 A | |
| L06-6012 | Fire Sprinkler Mains | 5 | 0 | 07-Apr-14 A | 30-Apr-14 A | |

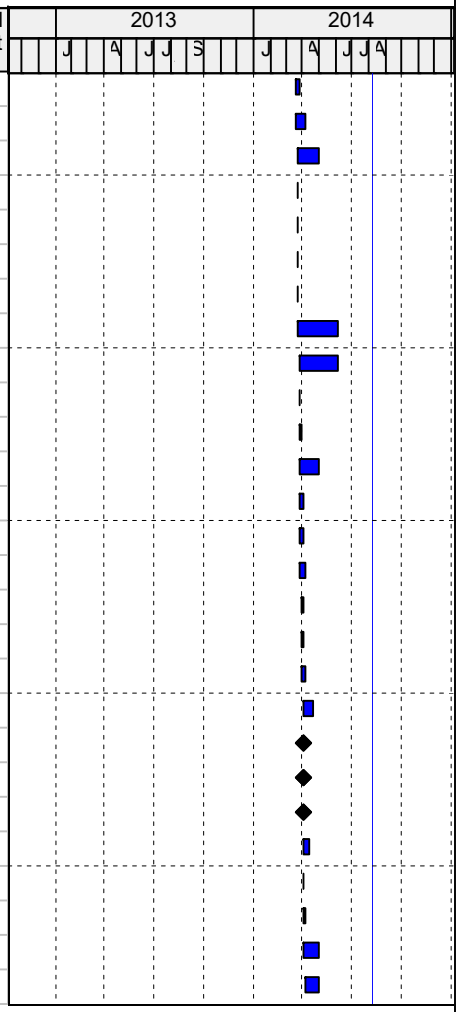



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L06-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L07-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| L07-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L03-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L03-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L04-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L06-6009 | Inspect Shafts | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L06-6019 | Complete Top Out GWB | 2 | 0 | 08-Apr-14 A | 18-Apr-14 A | |
| L07-6010 | Frame Walls | 5 | 0 | 08-Apr-14 A | 15-Apr-14 A | |
| L08-6011 | PreRock Shafts | 2 | 0 | 08-Apr-14 A | 23-Apr-14 A | |
| L09-6002 | Layout | 5 | 0 | 08-Apr-14 A | 26-Apr-14 A | |
| L03-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 09-Apr-14 A | 08-May-14 A | |
| L03-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L05-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 09-Apr-14 A | 14-Apr-14 A | |
| L08-6009 | Inspect Shafts | 1 | 0 | 09-Apr-14 A | 25-Apr-14 A | |
| L09-6008 | Frame Shaft Walls | 3 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| L08-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| L04-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 15-Apr-14 A | 16-Apr-14 A | |
| L07-6012 | Fire Sprinkler Mains | 5 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| L07-6016 | Electrical RI | 5 | 0 | 15-Apr-14 A | 12-May-14 A | |
| L07-6020 | Install Hollow Metal Frames | 3 | 0 | 16-Apr-14 A | 23-Apr-14 A | |
| L05-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 17-Apr-14 A | 25-Apr-14 A | |
| L06-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 17-Apr-14 A | 12-May-14 A | |
| L06-6023 | Inspection of Exterior Framing | 0 | 0 | 17-Apr-14 A | | |
| L09-8219 | HVAC Risers | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L09-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |

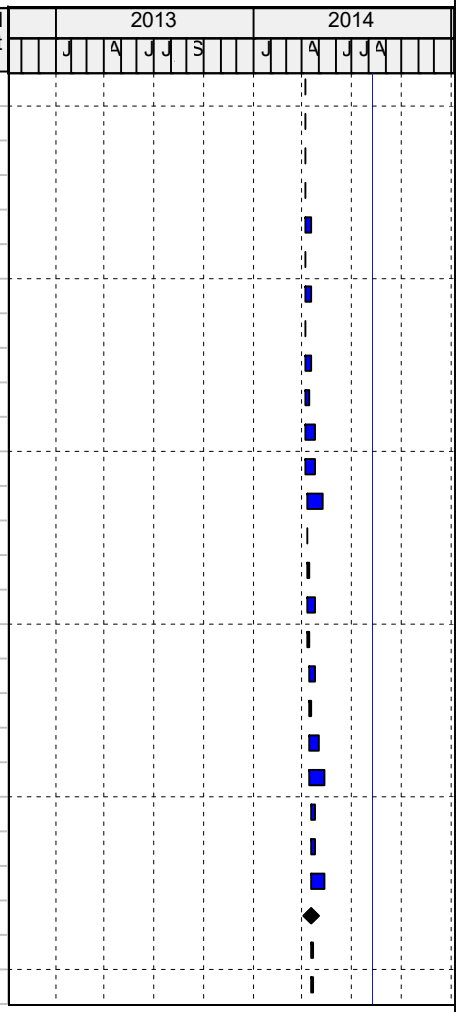



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 18-Apr-14 A | 20-Apr-14 A | |
| L04-6028 | PreRock at Heat Pumps | 2 | 0 | 20-Apr-14 A | 22-Apr-14 A | |
| L08-8219 | HVAC Risers | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6009 | Inspect Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6011 | PreRock Shafts | 2 | 0 | 22-Apr-14 A | 24-Apr-14 A | |
| L04-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L06-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 23-Apr-14 A | 25-Apr-14 A | |
| L08-6020 | Install Hollow Metal Frames | 3 | 0 | 23-Apr-14 A | 13-May-14 A | |
| L11-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L11-8220 | Plumbing Risers - Install | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L04-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L09-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L10-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L10-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 20-May-14 A | |
| L12-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L04-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 25-Apr-14 A | 11-Jun-14 A | |
| L04-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L09-6010 | Frame Walls | 5 | 0 | 25-Apr-14 A | 20-May-14 A | |
| L09-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L10-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L11-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 30-Apr-14 A | |
| L12-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L08-6010 | Frame Walls | 5 | 0 | 26-Apr-14 A | 30-Apr-14 A | |
| L10-6002 | Layout | 5 | 0 | 27-Apr-14 A | 27-Apr-14 A | |
| L04-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 28-Apr-14 A | 30-Apr-14 A | |

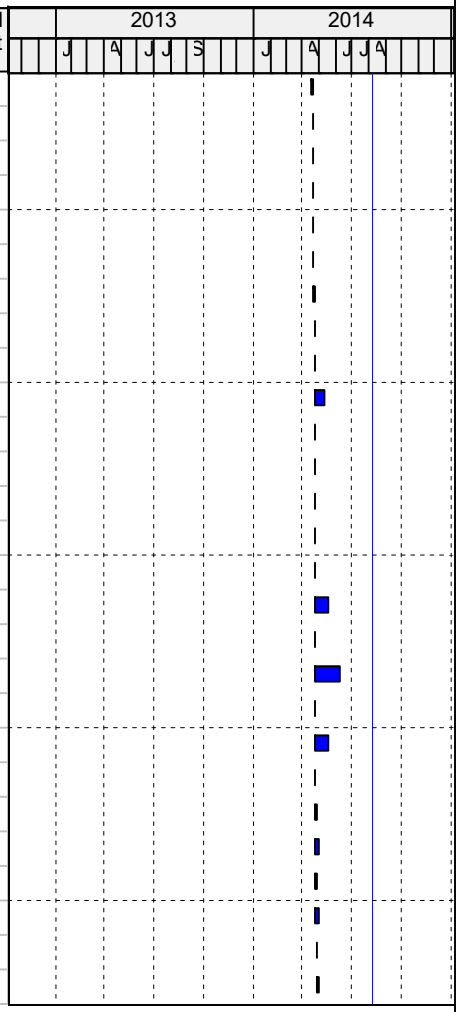



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6018 | HVAC RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6028 | PreRock at Heat Pumps | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L07-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 28-Apr-14 A | 12-May-14 A | |
| L10-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-Apr-14 A | 22-May-14 A | |
| L11-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L12-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L05-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| L05-6028 | PreRock at Heat Pumps | 2 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L06-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 09-May-14 A | |
| L06-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L06-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L08-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L08-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L09-6020 | Install Hollow Metal Frames | 3 | 0 | 29-Apr-14 A | 20-May-14 A | |
| L09-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L10-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L04-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 30-Apr-14 A | 02-May-14 A | |
| L09-6019 | Complete Top Out GWB | 2 | 0 | 30-Apr-14 A | 06-Jun-14 A | |
| L11-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |

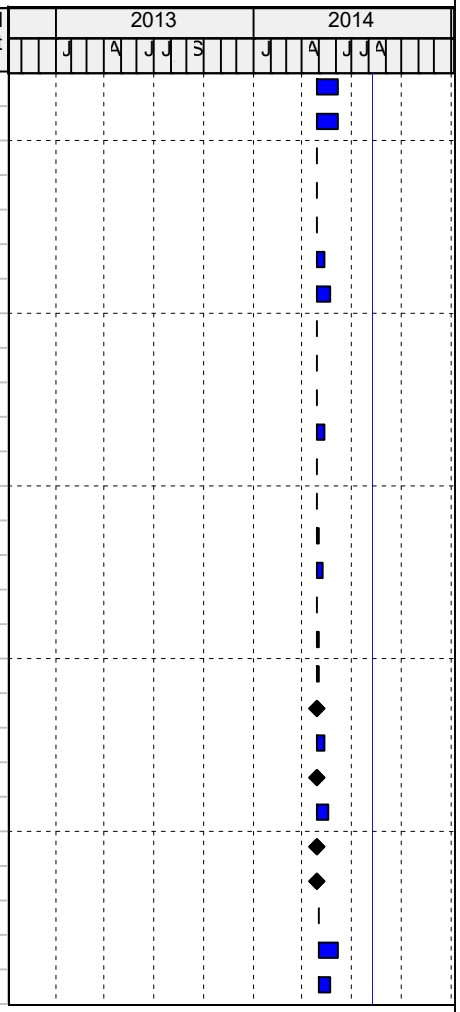



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L03-6028 | PreRock at Heat Pumps | 2 | 0 | 01-May-14 A | 02-May-14 A | |
| L05-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L06-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L03-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L05-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L05-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| L06-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L06-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 09-May-14 A | |
| L03-6018 | HVAC Rl | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L03-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 06-May-14 A | 06-May-14 A | |
| L07-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L07-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 06-May-14 A | 09-May-14 A | |
| L03-6004 | CMU Wall/Clips | 3 | 0 | 07-May-14 A | 08-May-14 A | |
| L03-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L03-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 08-May-14 A | 13-May-14 A | |
| L03-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6004 | CMU Walls | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6018 | HVAC Rl | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L11-6010 | Frame Walls | 5 | 0 | 09-May-14 A | 15-May-14 A | |
| L05-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 12-May-14 A | 05-Jun-14 A | |
| L07-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 12-May-14 A | 13-May-14 A | |

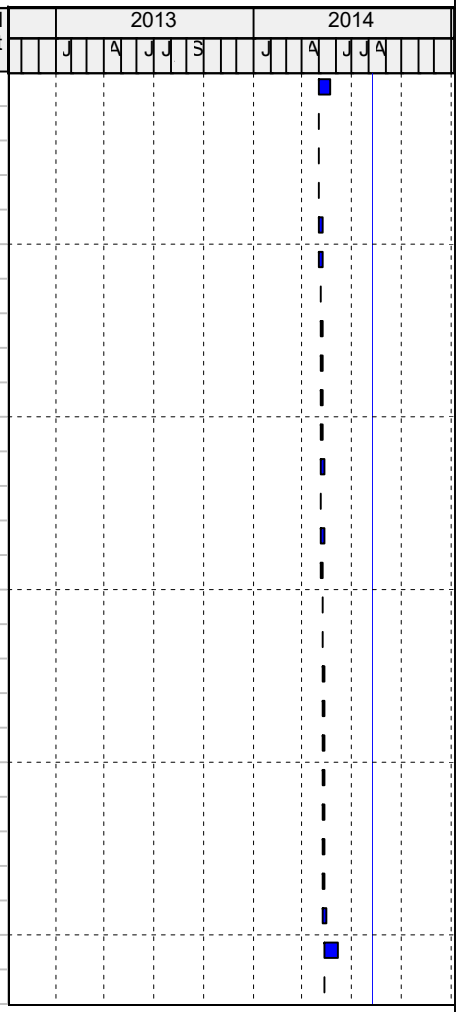



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6020 | Install Hollow Metal Frames | 3 | 0 | 12-May-14 A | 14-May-14 A | |
| L11-6019 | Complete Top Out GWB | 2 | 0 | 12-May-14 A | 14-May-14 A | |
| L14-6002 | Layout | 5 | 0 | 12-May-14 A | 14-May-14 A | |
| L15-6002 | Layout | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L05-6004 | CMU Walls | 3 | 0 | 13-May-14 A | 13-May-14 A | |
| L06-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 25-Jun-14 A | |
| L06-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 13-May-14 A | 14-Jul-14 A | |
| L07-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 05-Jun-14 A | |
| L07-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| L07-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 13-May-14 A | 13-May-14 A | |
| L14-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L16-6002 | Layout | 5 | 0 | 13-May-14 A | 16-May-14 A | |
| L06-6004 | CMU Walls | 3 | 0 | 14-May-14 A | 14-May-14 A | |
| L07-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 15-May-14 A | |
| L08-6012 | Fire Sprinkler Mains | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6002 | Layout | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L07-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6014 | Set Tubs & Plumbing RI | 5 | 0 | 16-May-14 A | 25-Jun-14 A | |
| L08-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L11-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L12-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L07-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L08-6028 | PreRock at Heat Pumps | 2 | 0 | 19-May-14 A | 20-May-14 A | |

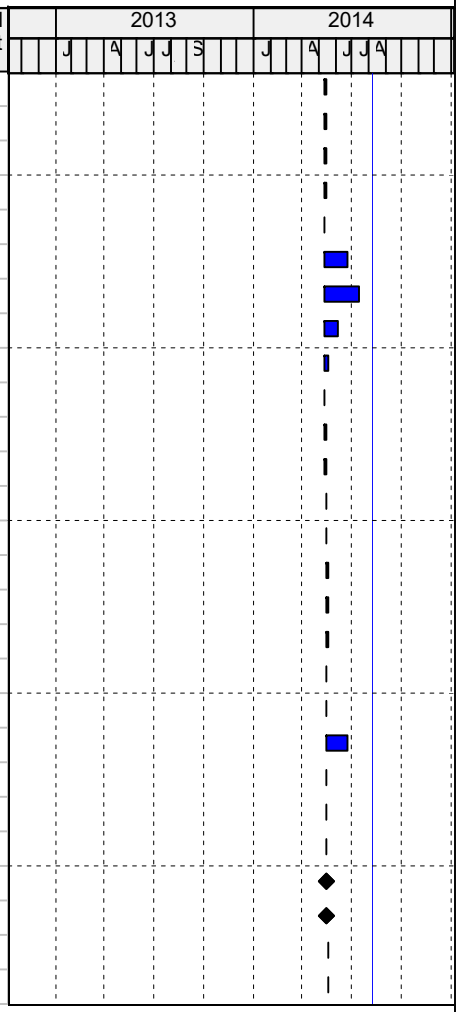



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L10-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L11-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L15-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 19-May-14 A | 19-May-14 A | |
| L07-6028 | PreRock at Heat Pumps | 2 | 0 | 20-May-14 A | 21-May-14 A | |
| L07-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L08-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 20-May-14 A | 21-May-14 A | |
| L10-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L11-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L14-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L07-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 21-May-14 A | 27-May-14 A | |
| L08-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L08-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L09-6028 | PreRock at Heat Pumps | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L10-6014 | Set Tubs & Plumbing RI | 5 | 0 | 21-May-14 A | 27-Jun-14 A | |
| L10-6010 | Frame Walls | 5 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6019 | Complete Top Out GWB | 2 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L11-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L12-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L14-8220 | Plumbing Risers - Install | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L15-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L16-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L07-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| L08-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 22-May-14 A | 22-May-14 A | |

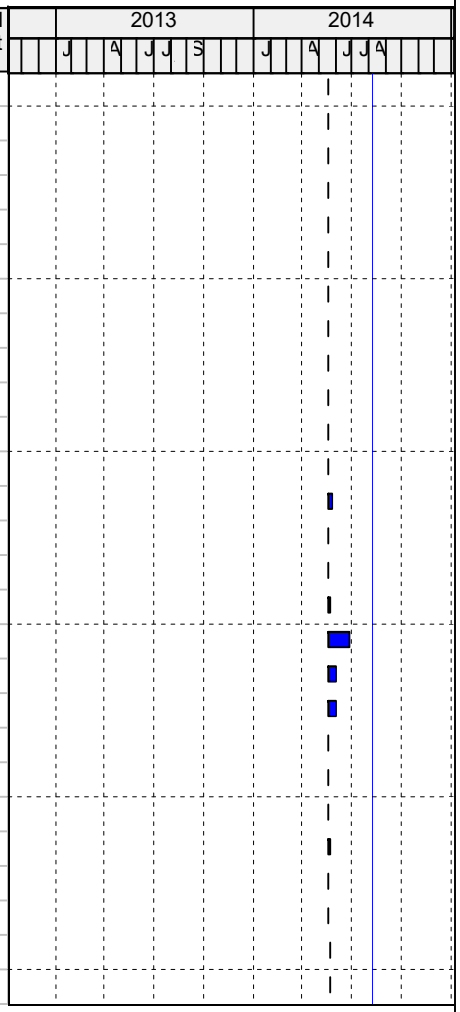



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-6012 | Fire Sprinkler Mains | 5 | 0 | 22-May-14 A | 27-May-14 A | |
| L08-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L09-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6020 | Install Hollow Metal Frames | 3 | 0 | 23-May-14 A | 03-Jun-14 A | |
| L10-6028 | PreRock at Heat Pumps | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L14-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L15-8220 | Plumbing Risers - Install | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L09-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 27-May-14 A | 27-May-14 A | |
| L12-6010 | Frame Walls | 5 | 0 | 27-May-14 A | 02-Jun-14 A | |
| L08-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L09-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 28-May-14 A | 28-May-14 A | |
| L10-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 28-May-14 A | 03-Jun-14 A | |
| L14-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L15-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-May-14 A | 30-May-14 A | |
| L16-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 28-May-14 A | 28-May-14 A | |
| L16-8220 | Plumbing Risers - Install | 2 | 0 | 28-May-14 A | 29-May-14 A | |
| L08-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 29-May-14 A | 30-May-14 A | |
| L10-6016 | Electrical RI | 5 | 1 | 29-May-14 A | 08-Aug-14 | 22 |
| L10-6022 | Fire Alarm / Elec Specialties RI | 4 | 1 | 29-May-14 A | 08-Aug-14 | 22 |
| L10-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L10-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| L12-6012 | Fire Sprinkler Mains | 5 | 0 | 30-May-14 A | 26-Jun-14 A | |
| L12-6020 | Install Hollow Metal Frames | 3 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L15-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L17-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L17-8220 | Plumbing Risers - Install | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L10-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 02-Jun-14 A | 03-Jun-14 A | |

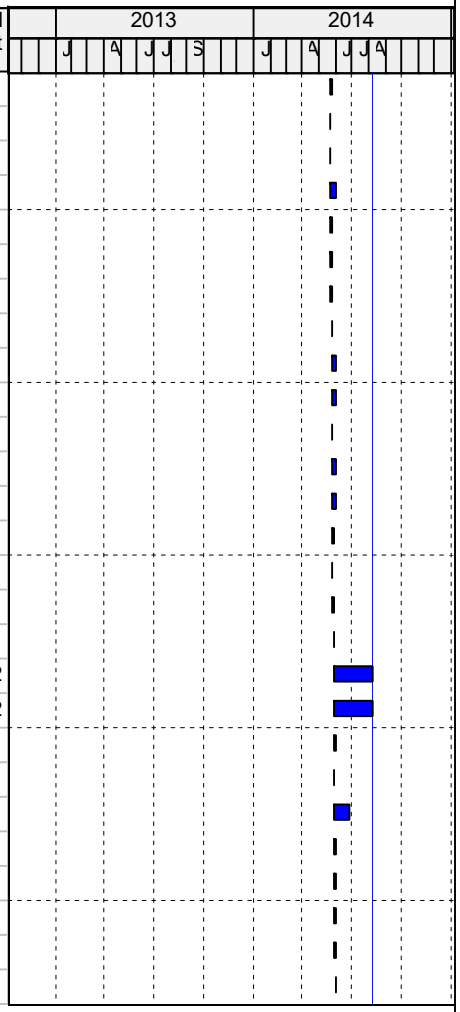



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6016 | Electrical RI | 5 | 3 | 02-Jun-14 A | 13-Aug-14 | 22 |
| L11-6022 | Fire Alarm / Elec Specialties RI | 4 | 3 | 02-Jun-14 A | 13-Aug-14 | 22 |
| L12-6019 | Complete Top Out GWB | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L14-6020 | Install Hollow Metal Frames | 3 | 0 | 02-Jun-14 A | 05-Jun-14 A | |
| L14-6010 | Frame Walls | 5 | 0 | 02-Jun-14 A | 04-Jun-14 A | |
| L16-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| L14-6019 | Complete Top Out GWB | 2 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L16-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L10-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| L17-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 04-Jun-14 A | 11-Jun-14 A | |
| L08-6016 | Electrical RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L08-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L09-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L12-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L15-6010 | Frame Walls | 3 | 0 | 05-Jun-14 A | 11-Jun-14 A | |
| L09-6012 | Fire Sprinkler Mains | 5 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L09-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L11-6012 | Fire Sprinkler Mains | 4 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L12-6014 | Set Tubs & Plumbing RI | 4 | 0 | 06-Jun-14 A | 27-Jun-14 A | |
| L11-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jun-14 A | 11-Jun-14 A | |
| L09-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-Jun-14 A | 25-Jun-14 A | |
| L14-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L15-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L16-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L09-6016 | Electrical RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |

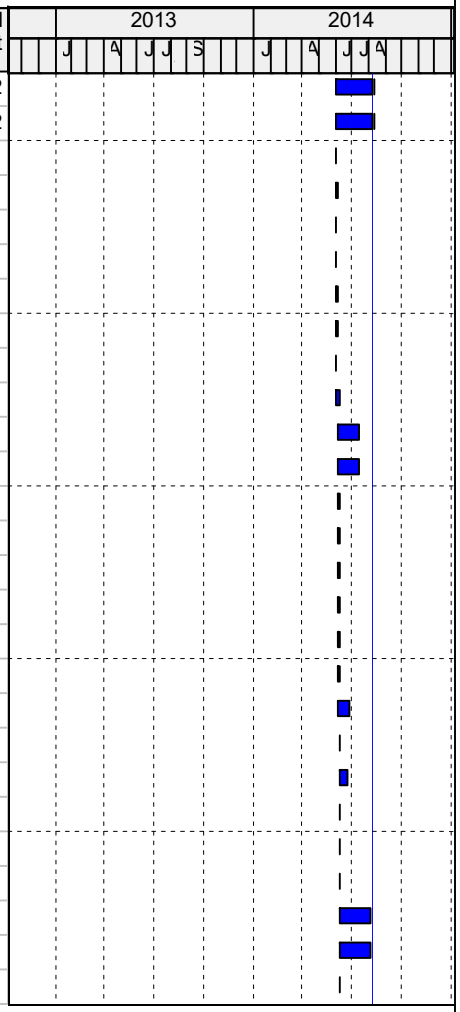



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L14-6014 | Set Tubs & Plumbing RI | 4 | 0 | 10-Jun-14 A | 21-Jul-14 A | |
| L15-6020 | Install Hollow Metal Frames | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L15-6019 | Complete Top Out GWB | 2 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6014 | Set Tubs & Plumbing RI | 4 | 0 | 11-Jun-14 A | 26-Jun-14 A | |
| L11-6028 | PreRock at Heat Pumps | 2 | 0 | 13-Jun-14 A | 14-Jun-14 A | |
| L11-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 14-Jun-14 A | 14-Jun-14 A | |
| L14-6012 | Fire Sprinkler Mains | 2 | 0 | 16-Jun-14 A | 27-Jun-14 A | |
| L14-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 18-Jun-14 A | 18-Jun-14 A | |
| L15-6023 | Inspection of Exterior Framing | 0 | 0 | 18-Jun-14 A | | |
| L17-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 18-Jun-14 A | 23-Jun-14 A | |
| L17-6010 | Frame Walls | 5 | 0 | 18-Jun-14 A | 29-Jul-14 A | |
| L10-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L12-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6023 | Inspection of Exterior Framing | 0 | 0 | 20-Jun-14 A | | |
| L15-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-Jun-14 A | 20-Jun-14 A | |
| L10-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-Jun-14 A | 23-Jun-14 A | |
| L15-6014 | Set Tubs & Plumbing RI | 5 | 0 | 22-Jun-14 A | 24-Jul-14 A | |
| L08-6018 | HVAC RI | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L12-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L14-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L15-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L08-6221 | Frame Unit Ceilings | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| L11-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 24-Jun-14 A | 27-Jun-14 A | |

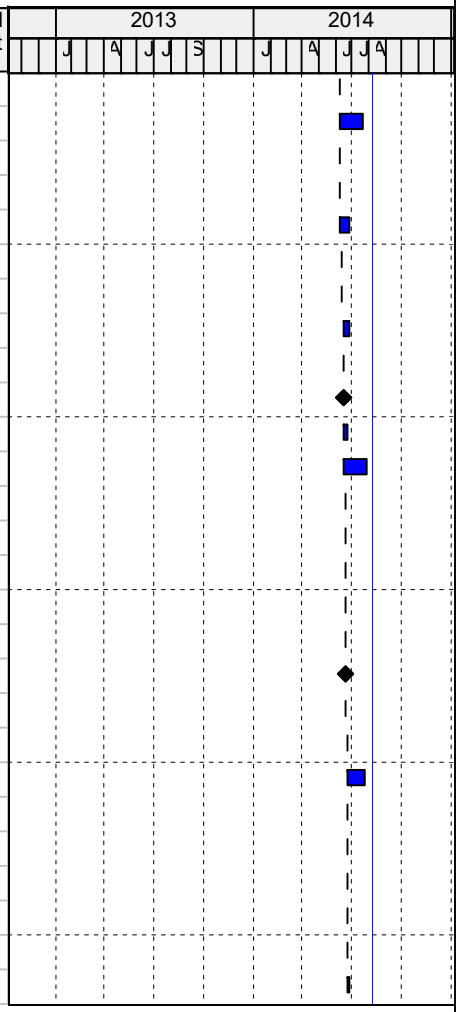


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L14-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6023 | Inspection of Exterior Framing | 0 | 0 | 24-Jun-14 A | | |
| L12-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| L12-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L14-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L15-6012 | Fire Sprinkler Mains | 2 | 0 | 25-Jun-14 A | 22-Jul-14 A | |
| L16-6023 | Inspection of Exterior Framing | 0 | 0 | 25-Jun-14 A | | |
| L03-6024 | Inspections for GWB Cover | 1 | 0 | 27-Jun-14 A | 27-Jun-14 A | |
| L09-6018 | HVAC RI | 3 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L09-6221 | Frame Unit Ceilings | 2 | 0 | 27-Jun-14 A | 30-Jun-14 A | |
| L12-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L14-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L15-6028 | PreRock at Heat Pumps | 2 | 0 | 30-Jun-14 A | 01-Jul-14 A | |
| L16-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 30-Jun-14 A | 30-Jun-14 A | |
| L16-6010 | Frame Walls | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| L16-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L15-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L15-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L04-6024 | Inspections for GWB Cover | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L10-6018 | HVAC RI | 3 | 0 | 07-Jul-14 A | 21-Jul-14 A | |
| L11-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L15-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L16-6012 | Fire Sprinkler Mains | 2 | 0 | 07-Jul-14 A | 24-Jul-14 A | |
| L16-6020 | Install Hollow Metal Frames | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L16-6028 | PreRock at Heat Pumps | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L17-6019 | Complete Top Out GWB | 1 | 1 | 07-Jul-14 A | 08-Aug-14 | 26 |

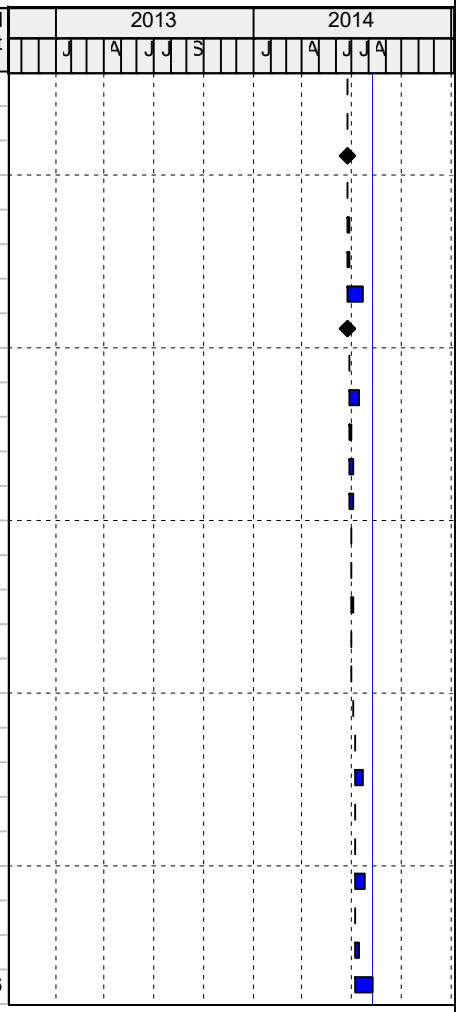



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L15-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 08-Jul-14 A | 04-Aug-14 A | |
| L17-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jul-14 A | 01-Aug-14 A | |
| L10-6221 | Frame Unit Ceilings | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| L17-6012 | Fire Sprinkler Mains | 2 | 2 | 09-Jul-14 A | 12-Aug-14 | 26 |
| L05-6024 | Inspections for GWB Cover | 2 | 0 | 10-Jul-14 A | 10-Jul-14 A | |
| L04-6000 | Tape/Finish GWB | 6 | 0 | 11-Jul-14 A | 23-Jul-14 A | |
| L16-6019 | Complete Top Out GWB | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L16-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L15-6018 | HVAC RI | 3 | 0 | 16-Jul-14 A | 18-Jul-14 A | |
| L16-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-6024 | Inspections for GWB Cover | 2 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6018 | HVAC RI | 3 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L16-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 1 | 21-Jul-14 A | 08-Aug-14 | 35 |
| L15-6013 | Fire Sprinkler Branch Lines | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| L03-6000 | Tape/Finish GWB | 6 | 0 | 23-Jul-14 A | 29-Jul-14 A | |
| L11-6018 | HVAC RI | 3 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L15-6221 | Frame Unit Ceilings | 2 | 0 | 23-Jul-14 A | 01-Aug-14 A | |
| L16-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L17-6020 | Install Hollow Metal Frames | 3 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| L11-6221 | Frame Unit Ceilings | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6016 | Electrical RI | 5 | 4 | 28-Jul-14 A | 19-Aug-14 | 22 |
| L12-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6022 | Fire Alarm / Elec Specialties RI | 5 | 4 | 28-Jul-14 A | 19-Aug-14 | 22 |
| L14-6016 | Electrical RI | 5 | 5 | 28-Jul-14 A | 22-Aug-14 | 22 |
| L14-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |

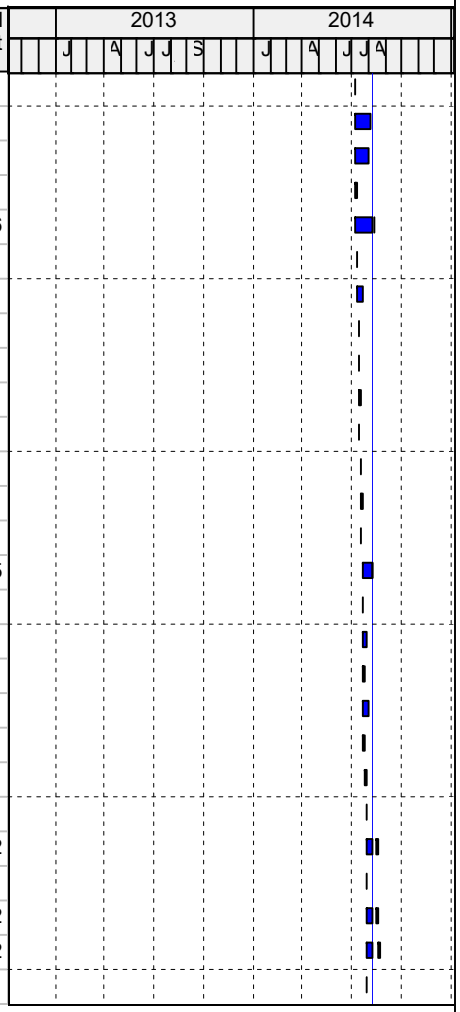



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6022 | Fire Alarm / Elec Specialties Rl | 5 | 5 | 28-Jul-14 A | 22-Aug-14 | 22 |
| L16-6014 | Set Tubs & Plumbing Rl | 5 | 1 | 28-Jul-14 A | 08-Aug-14 | 29 |
| L07-6024 | Inspections for GWB Cover | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L12-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L05-6000 | Tape/Finish GWB | 6 | 0 | 31-Jul-14 A | 05-Aug-14 A | |
| L08-6024 | Inspections for GWB Cover | 2 | 0 | 31-Jul-14 A | 31-Jul-14 A | |
| L12-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L14-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L06-6000 | Tape/Finish GWB | 4 | 3 | 06-Aug-14 A | 11-Aug-14 | 24 |
| L09-6024 | Inspections for GWB Cover | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L07-6000 | Tape/Finish GWB | 5 | 5 | 07-Aug-14 A | 18-Aug-14 | 20 |
| L11-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 22 |
| L16-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 36 |
| L17-6014 | Set Tubs & Plumbing Rl | 5 | 5 | 08-Aug-14 | 14-Aug-14 | 26 |
| L10-6024 | Inspections for GWB Cover | 2 | 2 | 11-Aug-14 | 12-Aug-14 | 22 |
| L09-6000 | Tape/Finish GWB | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 23 |
| L17-6013 | Fire Sprinkler Branch Lines | 2 | 2 | 13-Aug-14 | 14-Aug-14 | 26 |
| L11-6024 | Inspections for GWB Cover | 2 | 2 | 14-Aug-14 | 15-Aug-14 | 22 |
| L08-6000 | Tape/Finish GWB | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 19 |
| L17-6018 | HVAC Rl | 3 | 3 | 15-Aug-14 | 19-Aug-14 | 26 |
| L10-6000 | Tape/Finish GWB | 5 | 5 | 19-Aug-14 | 23-Aug-14 | 27 |
| L17-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 1 | 19-Aug-14 | 19-Aug-14 | 22 |
| L12-6024 | Inspections for GWB Cover | 2 | 2 | 20-Aug-14 | 21-Aug-14 | 22 |
| L17-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 1 | 20-Aug-14 | 20-Aug-14 | 22 |
| L17-6028 | PreRock at Heat Pumps | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 22 |

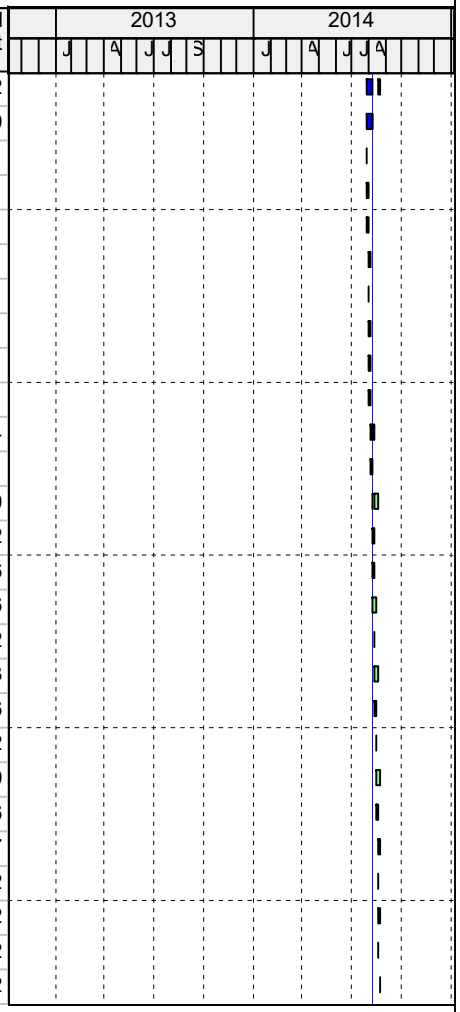


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6000 | Tape/Finish GWB | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 21 |
| L15-6016 | Electrical RI | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 22 |
| L15-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 22 |
| L16-6221 | Frame Unit Ceilings | 4 | 4 | 22-Aug-14 | 26-Aug-14 | 25 |
| L14-6024 | Inspections for GWB Cover | 2 | 2 | 25-Aug-14 | 26-Aug-14 | 22 |
| L17-6029 | Inspection of PreRock at Heat Pumps | 1 | 1 | 25-Aug-14 | 25-Aug-14 | 22 |
| L17-6030 | Tape/Firecaulk at Heat Pumps | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 22 |
| L16-6016 | Electrical RI | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 22 |
| L16-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 22 |
| L17-6221 | Frame Unit Ceilings | 4 | 4 | 27-Aug-14 | 02-Sep-14 | 21 |
| L17-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 1 | 27-Aug-14 | 27-Aug-14 | 22 |
| L12-6000 | Tape/Finish GWB | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 21 |
| L17-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 3 | 28-Aug-14 | 02-Sep-14 | 22 |
| L15-6024 | Inspections for GWB Cover | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 22 |
| L17-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 22 |
| L17-6016 | Electrical RI | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 21 |
| L17-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 21 |
| L14-6000 | Tape/Finish GWB | 5 | 5 | 04-Sep-14 | 09-Sep-14 | 25 |
| L16-6024 | Inspections for GWB Cover | 2 | 2 | 04-Sep-14 | 05-Sep-14 | 22 |
| L15-6000 | Tape/Finish GWB | 4 | 4 | 10-Sep-14 | 13-Sep-14 | 25 |
| L17-6024 | Inspections for GWB Cover | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 21 |
| L16-6000 | Tape/Finish GWB | 4 | 4 | 13-Sep-14 | 17-Sep-14 | 25 |
| L17-6000 | Tape/Finish GWB | 6 | 6 | 18-Sep-14 | 24-Sep-14 | 25 |
| **Mechanical Penthouse** | | | | | | |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 0 | 11-Jun-14 A | 20-Jun-14 A | |
| PH-6006 | PH - Exterior Wall Framing (including PH roof parapet | 6 | 0 | 12-Jun-14 A | 14-Jul-14 A | |
| PH-6014 | PH - Plumbing/Piping RI | 40 | 18 | 25-Jun-14 A | 08-Sep-14 | 8 |

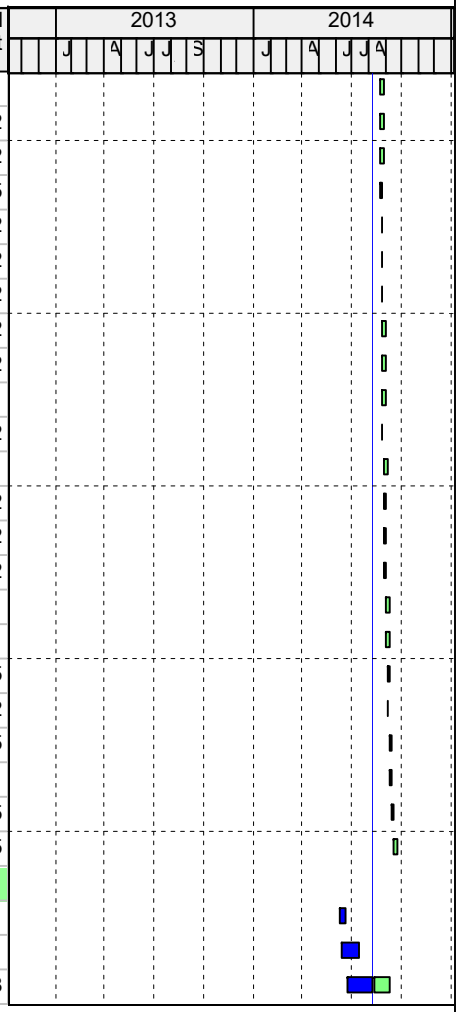



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-6002 | PH - Layout | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| PH-6008 | PH - Interior Wall Framing | 3 | 1 | 24-Jul-14 A | 08-Aug-14 | 8 |
| PH-6020 | PH - H Mtl Frames | 2 | 2 | 08-Aug-14 | 11-Aug-14 | 34 |
| PH-6012 | PH - Fire Sprinkler Rl | 10 | 10 | 02-Sep-14 | 15-Sep-14 | 8 |
| PH-6016 | PH - Electrical Rl | 10 | 10 | 02-Sep-14 | 15-Sep-14 | 8 |
| PH-6018 | PH - HVAC Rl | 10 | 10 | 02-Sep-14 | 15-Sep-14 | 8 |
| PH-6022 | PH - Fire Alarm / Elec Specialties Rl | 10 | 10 | 02-Sep-14 | 15-Sep-14 | 8 |
| PH-6024 | PH - Inspections | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 8 |
| **Finishes** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL4-8100 | LL4 - Insulation | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 58 |
| LL4-8102 | LL4 - GWB Hang / Tape / Finish | 8 | 8 | 14-Aug-14 | 25-Aug-14 | 58 |
| LL4-8104 | LL4 - Int Painting | 2 | 2 | 26-Aug-14 | 27-Aug-14 | 58 |
| LL4-8122 | LL4 - Plumbing Trim / Finish | 3 | 3 | 28-Aug-14 | 02-Sep-14 | 65 |
| LL4-8108 | LL4 - Elec Trim / Finish | 3 | 3 | 28-Aug-14 | 02-Sep-14 | 65 |
| LL4-8110 | LL4 - HVAC Trim / Finish | 3 | 3 | 28-Aug-14 | 02-Sep-14 | 65 |
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 3 | 3 | 28-Aug-14 | 02-Sep-14 | 66 |
| LL4-8124 | LL4 - Flooring (VCT) | 4 | 4 | 28-Aug-14 | 03-Sep-14 | 58 |
| LL4-8118 | LL4 - Elec Specialties Trim / Finish | 3 | 3 | 28-Aug-14 | 02-Sep-14 | 66 |
| LL4-8126 | LL4 - Doors & Hardware | 3 | 3 | 02-Sep-14 | 04-Sep-14 | 58 |
| LL4-8114 | LL4 - Striping / Signage | 5 | 5 | 05-Sep-14 | 11-Sep-14 | 58 |
| LL4-8130 | LL4 - Substantially Complete | 0 | 0 | | 11-Sep-14 | 58 |
| LL4-8132 | LL4 - Punch | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 58 |
| LL4-8134 | LL4 - Clean | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 58 |
| LL4-8210 | LL4 - Owner Walk / Create Punchlist | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 58 |

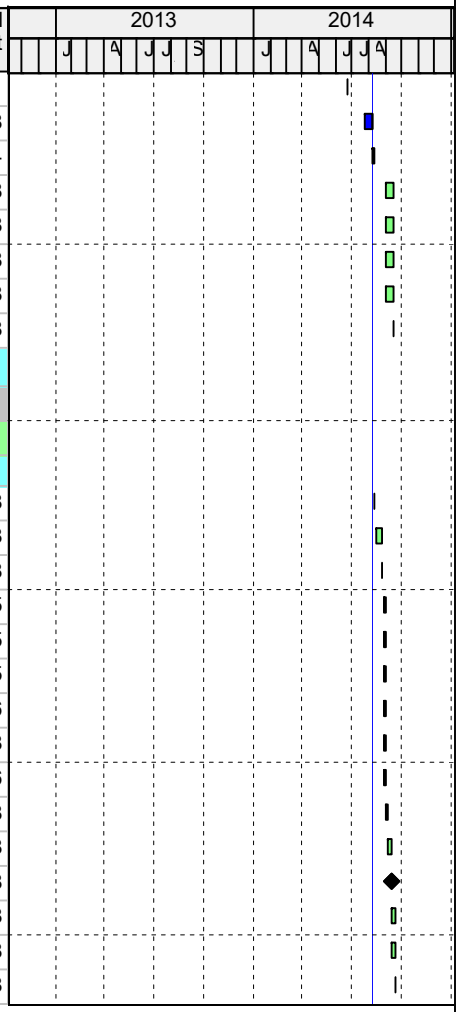



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8212 | LL4 - Resolve Final Punchlist | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 58 |
| LL4-8214 | LL4 - Floor Complete | 0 | 0 | | 26-Sep-14 | 58 |
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL3-8100 | LL3 - Insulation | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 53 |
| LL3-8102 | LL3 - GWB Hang / Tape / Finish | 8 | 8 | 14-Aug-14 | 25-Aug-14 | 53 |
| LL3-8104 | LL3 - Int Painting | 2 | 2 | 26-Aug-14 | 27-Aug-14 | 53 |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 3 | 3 | 28-Aug-14 | 02-Sep-14 | 60 |
| LL3-8108 | LL3 - Elec Trim / Finish | 3 | 3 | 28-Aug-14 | 02-Sep-14 | 60 |
| LL3-8110 | LL3 - HVAC Trim / Finish | 3 | 3 | 28-Aug-14 | 02-Sep-14 | 60 |
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 3 | 3 | 28-Aug-14 | 02-Sep-14 | 66 |
| LL3-8124 | LL3 - Flooring (VCT) | 4 | 4 | 28-Aug-14 | 03-Sep-14 | 53 |
| LL3-8118 | LL3 - Elec Specialties Trim / Finish | 3 | 3 | 28-Aug-14 | 02-Sep-14 | 66 |
| LL3-8126 | LL3 - Doors & Hardware | 3 | 3 | 02-Sep-14 | 04-Sep-14 | 53 |
| LL3-8114 | LL3 - Striping / Signage | 5 | 5 | 05-Sep-14 | 11-Sep-14 | 53 |
| LL3-8130 | LL3 - Substantially Complete | 0 | 0 | | 11-Sep-14 | 53 |
| LL3-8132 | LL3 - Punch | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 53 |
| LL3-8134 | LL3 - Clean | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 53 |
| LL3-8210 | LL3 - Owner Walk / Create Punchlist | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 53 |
| LL3-8212 | LL3 - Resolve Final Punchlist | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 53 |
| LL3-8214 | LL3 - Floor Complete | 0 | 0 | | 26-Sep-14 | 53 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 4 | 3 | 02-Jun-14 A | 12-Aug-14 | 76 |
| LL2E-8102 | LL2 - GWB Hang / Tape / Finish @ Electrical Rooms | 8 | 0 | 24-Jun-14 A | 03-Jul-14 A | |
| LL2-8100 | LL2 - Insulation | 3 | 3 | 14-Aug-14 | 18-Aug-14 | 29 |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish | 5 | 5 | 19-Aug-14 | 25-Aug-14 | 29 |

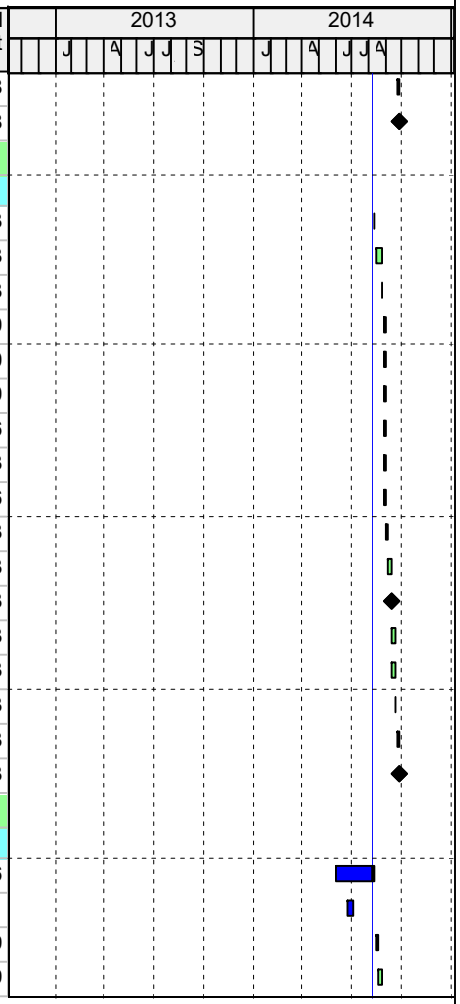



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-8104 | LL2 - Int Painting | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 29 |
| LL2-8136 | LL2 - Chainlink Fencing / Gate @ Recycling | 3 | 3 | 29-Aug-14 | 03-Sep-14 | 64 |
| LL2-8116 | LL2 - Finish Carpentry / Millwork | 3 | 3 | 02-Sep-14 | 04-Sep-14 | 54 |
| LL2-8128 | LL2 - Entry Gates | 3 | 3 | 02-Sep-14 | 04-Sep-14 | 63 |
| LL2-8108 | LL2 - Elec Trim / Finish | 3 | 3 | 03-Sep-14 | 05-Sep-14 | 51 |
| LL2-8112 | LL2 - Fire Sprinkler Trim / Finish | 2 | 2 | 03-Sep-14 | 04-Sep-14 | 54 |
| LL2-8118 | LL2 - Elec Specialties Trim / Finish | 3 | 3 | 03-Sep-14 | 05-Sep-14 | 53 |
| LL2-8122 | LL2 - Plumbing Trim / Finish | 3 | 3 | 04-Sep-14 | 08-Sep-14 | 51 |
| LL2-8120 | LL2 - Steel Pipe Guardrails & Bollards | 3 | 3 | 05-Sep-14 | 09-Sep-14 | 56 |
| LL2-8110 | LL2 - HVAC Trim / Finish | 3 | 3 | 08-Sep-14 | 10-Sep-14 | 51 |
| LL2-8114 | LL2 - Striping / Signage | 4 | 4 | 10-Sep-14 | 15-Sep-14 | 56 |
| LL2-8124 | LL2 - Flooring | 4 | 4 | 10-Sep-14 | 15-Sep-14 | 51 |
| LL2-8126 | LL2 - Doors & Hardware | 3 | 3 | 15-Sep-14 | 17-Sep-14 | 54 |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 5 | 5 | 16-Sep-14 | 22-Sep-14 | 51 |
| LL2-8130 | LL2 - Substantially Complete | 0 | 0 | | 22-Sep-14 | 51 |
| LL2-8132 | LL2 - Punch | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 51 |
| LL2-8134 | LL2 - Clean | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 51 |
| LL2-8210 | LL2 - Owner Walk / Create Punchlist | 1 | 1 | 30-Sep-14 | 30-Sep-14 | 51 |
| LL2-8212 | LL2 - Resolve Final Punchlist | 5 | 5 | 01-Oct-14 | 07-Oct-14 | 51 |
| LL2-8214 | LL2 - Floor Complete | 0 | 0 | | 07-Oct-14 | 51 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 31-Jul-14 A | |
| LL1-Z2U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 09-May-14 A | |
| LL1-Z3U-8102 | Above Ceiling GWB (At All Areas North of Q-Line) | 5 | 0 | 10-Feb-14 A | 20-Jun-14 A | |
| L1BU-8102 | Above Ceiling GWB [including East Service Corridor] | 5 | 0 | 06-Jun-14 A | 11-Jun-14 A | |
| L1LU-8102 | Above Ceiling GWB | 5 | 4 | 24-Jun-14 A | 03-Sep-14 | 1 |

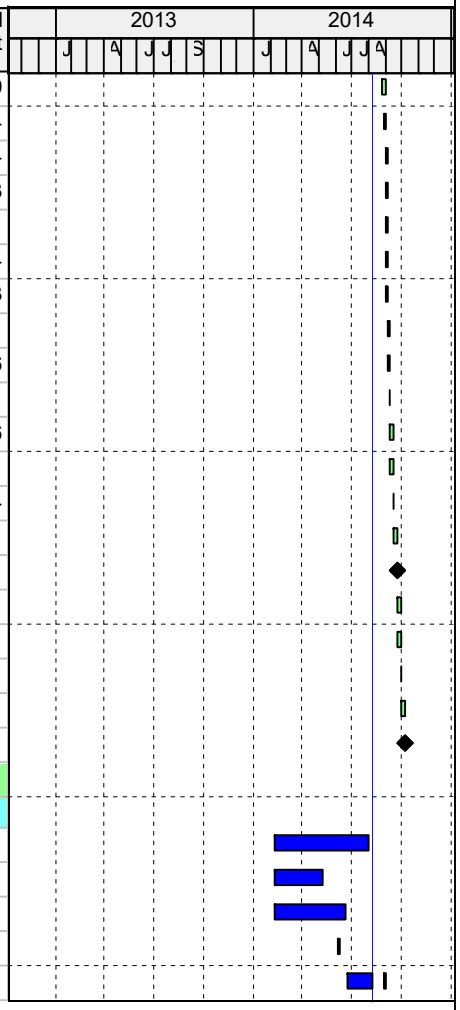



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1KU-8102 | Above Ceiling GWB | 2 | 1 | 26-Jun-14 A | 22-Aug-14 | 13 |
| LL1-8100 | Insulation | 5 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| LL1-8102 | GWB Hang (Walls) & Inspection | 5 | 1 | 28-Jul-14 A | 08-Aug-14 | 29 |
| LL1-8215 | GWB Tape (Walls) | 7 | 7 | 09-Aug-14 | 16-Aug-14 | 36 |
| LL1-Z2-8102 | GWB Hang (Walls) & Inspection | 4 | 4 | 11-Aug-14 | 14-Aug-14 | 24 |
| LL1-Z2-8100 | Insulation | 3 | 3 | 11-Aug-14 | 13-Aug-14 | 24 |
| LL1-Z3-8100 | Insulation | 5 | 5 | 13-Aug-14 | 19-Aug-14 | 30 |
| LL1-Z3-8102 | GWB Hang (Walls) & Inspection | 5 | 5 | 14-Aug-14 | 20-Aug-14 | 30 |
| L1B-8100 | Insulation | 5 | 5 | 20-Aug-14 | 26-Aug-14 | 8 |
| L1B-8102 | GWB Hang (Walls) & Inspection | 8 | 8 | 21-Aug-14 | 02-Sep-14 | 8 |
| LL1-Z3-8215 | GWB Tape (Walls & Ceilings) | 7 | 7 | 28-Aug-14 | 08-Sep-14 | 30 |
| L1K-8100 | Insulation | 5 | 5 | 29-Aug-14 | 05-Sep-14 | 11 |
| L1K-8102 | GWB Hang (Walls) & Inspection | 11 | 11 | 02-Sep-14 | 16-Sep-14 | 11 |
| L1B-8215 | GWB Tape (Walls) | 6 | 6 | 03-Sep-14 | 10-Sep-14 | 8 |
| LL1-Z3-8104 | Prime Paint | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 30 |
| L1L-8100 | Insulation | 4 | 4 | 09-Sep-14 | 12-Sep-14 | 0 |
| L1L-8102 | GWB Hang (Walls) | 4 | 4 | 10-Sep-14 | 15-Sep-14 | 0 |
| LL1-Z3-8114 | T Bar Grid Ceiling & Inspection | 6 | 6 | 11-Sep-14 | 18-Sep-14 | 30 |
| LL1-Z2-8215 | GWB Tape (Walls/Ceilings) | 7 | 7 | 15-Sep-14 | 23-Sep-14 | 24 |
| L1L-8215 | GWB Tape (Walls) | 7 | 7 | 16-Sep-14 | 24-Sep-14 | 0 |
| L1K-8215 | GWB Tape (Walls & Ceilings) | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 11 |
| LL1-8104 | Prime Paint | 3 | 3 | 18-Sep-14 | 22-Sep-14 | 30 |
| LL1-8114 | T Bar Grid Ceiling & Inspection | 3 | 3 | 23-Sep-14 | 25-Sep-14 | 30 |
| LL1-Z2-8104 | Prime Paint | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 24 |
| LL1-Z3-8140 | Acoustical Ceiling Tile | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 30 |
| LL1-Z2-8114 | T Bar Grid Ceiling & Inspection | 3 | 3 | 26-Sep-14 | 30-Sep-14 | 24 |
| LL1-Z3-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 29-Sep-14 | 01-Oct-14 | 30 |

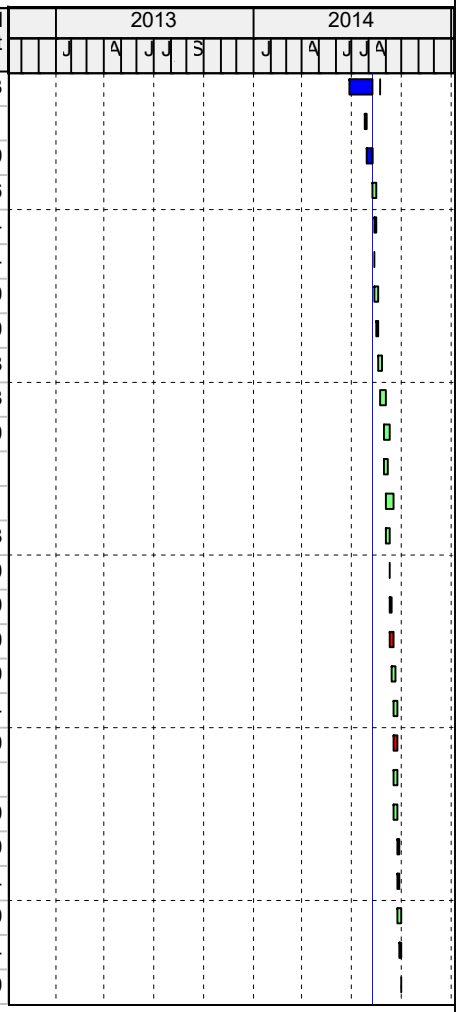



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 29-Sep-14 | 01-Oct-14 | 30 |
| L1K-8104 | Prime Paint | 3 | 3 | 30-Sep-14 | 02-Oct-14 | 11 |
| LL1-Z2-8106 | Wallcoverings | 4 | 4 | 02-Oct-14 | 07-Oct-14 | 24 |
| LL1-Z3-8124 | Flooring (Epoxy) | 8 | 8 | 02-Oct-14 | 10-Oct-14 | 37 |
| LL1-8124 | Flooring | 4 | 4 | 03-Oct-14 | 08-Oct-14 | 30 |
| L1K-8106 | Wallcoverings (FRP) | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 11 |
| L1K-8114 | T Bar Grid Ceiling | 4 | 4 | 03-Oct-14 | 08-Oct-14 | 19 |
| LL1-Z2-8124 | Flooring | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 24 |
| LL1-8116 | Finish Carpentry / Millwork | 5 | 5 | 08-Oct-14 | 14-Oct-14 | 30 |
| LL1-8126 | Doors & Hardware | 5 | 5 | 08-Oct-14 | 14-Oct-14 | 30 |
| LL1-8140 | Acoustical Ceiling Tile | 5 | 5 | 08-Oct-14 | 14-Oct-14 | 30 |
| LL1-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 10-Oct-14 | 14-Oct-14 | 30 |
| LL1-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 10-Oct-14 | 14-Oct-14 | 30 |
| LL1-Z3-8116 | Finish Carpentry / Millwork | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 31 |
| LL1-Z3-8126 | Doors & Hardware | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 29 |
| LL1-Z2-8116 | Finish Carpentry / Millwork | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 24 |
| LL1-Z2-8126 | Doors & Hardware | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 26 |
| LL1-Z2-8140 | Acoustical Ceiling Tile | 3 | 3 | 16-Oct-14 | 20-Oct-14 | 24 |
| L1K-8140 | Acoustical Ceiling Tile | 4 | 4 | 16-Oct-14 | 21-Oct-14 | 11 |
| L1B-8104 | Prime Paint | 3 | 3 | 17-Oct-14 | 21-Oct-14 | 8 |
| LL1-Z2-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 20-Oct-14 | 21-Oct-14 | 25 |
| LL1-Z2-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 24 |
| L1K-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 11 |
| L1K-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 11 |
| L1K-8124 | Flooring (VCT & Tile) | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 11 |
| LL1-8132 | Punch | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 30 |
| LL1-8134 | Clean | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 30 |

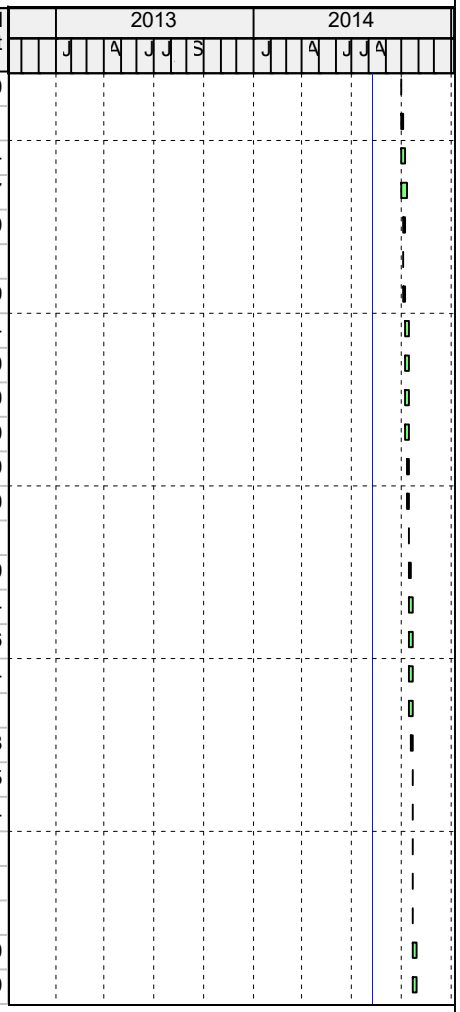



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-8114 | T Bar Grid Ceiling | 2 | 2 | 22-Oct-14 | 23-Oct-14 | 8 |
| LL1-Z3-8132 | Punch | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 29 |
| LL1-Z3-8134 | Clean | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 29 |
| LL1-Z2-8132 | Punch | 5 | 5 | 30-Oct-14 | 05-Nov-14 | 24 |
| LL1-Z2-8134 | Clean | 5 | 5 | 30-Oct-14 | 05-Nov-14 | 24 |
| L1B-8124 | Flooring (Carpet) | 4 | 4 | 31-Oct-14 | 05-Nov-14 | 8 |
| L1L-8104 | Prime Paint | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 0 |
| L1K-8116 | Finish Carpentry / Millwork | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 9 |
| L1K-8126 | Doors & Hardware | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 9 |
| L1B-8116 | Finish Carpentry / Millwork | 4 | 4 | 06-Nov-14 | 12-Nov-14 | 11 |
| L1B-8126 | Doors & Hardware | 4 | 4 | 06-Nov-14 | 12-Nov-14 | 11 |
| L1B-8140 | Acoustical Ceiling Tile | 4 | 4 | 06-Nov-14 | 12-Nov-14 | 8 |
| L1L-8114 | Install wood ceiling supports | 2 | 2 | 06-Nov-14 | 07-Nov-14 | 0 |
| L1L-8106 | Wallcoverings | 5 | 5 | 11-Nov-14 | 17-Nov-14 | 0 |
| L1B-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 12-Nov-14 | 17-Nov-14 | 8 |
| L1B-8118 | Elec & Specialties Trim / Finish | 4 | 4 | 12-Nov-14 | 17-Nov-14 | 8 |
| L1K-8132 | Punch | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 9 |
| L1K-8134 | Clean | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 9 |
| L1L-8124 | Flooring | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 0 |
| L1L-8140 | Install wood ceiling | 6 | 6 | 21-Nov-14 | 02-Dec-14 | 0 |
| L1B-8132 | Punch | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 8 |
| L1B-8134 | Clean | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 8 |
| L1L-8116 | Finish Carpentry / Millwork | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 0 |
| L1L-8126 | Doors & Hardware | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 0 |
| L1L-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 0 |
| L1L-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 0 |
| L1L-8132 | Punch | 4 | 4 | 10-Dec-14 | 15-Dec-14 | 0 |

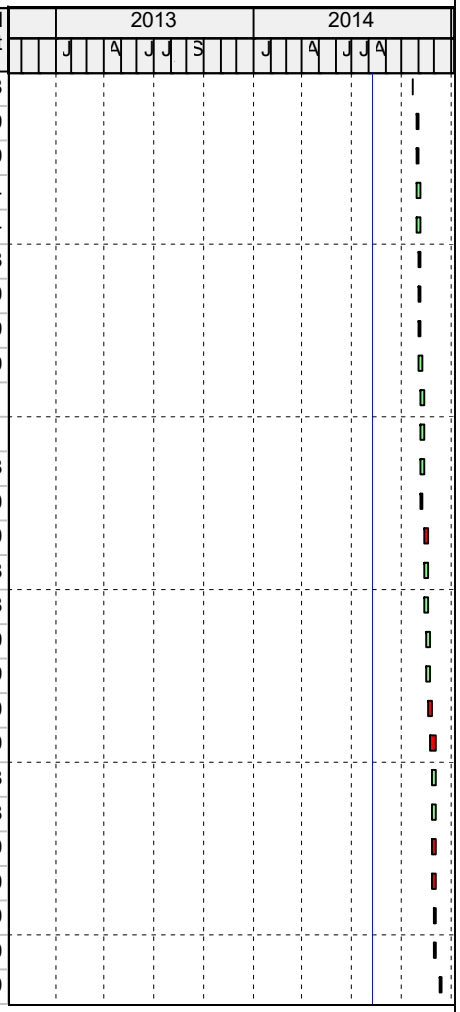



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8134 | Clean | 4 | 4 | 10-Dec-14 | 15-Dec-14 | 0 |
| **Corridors / Common / Public Areas** | | | | | | |
| LL1-Z3-8200 | First Coat Finish Paint | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 30 |
| LL1-8200 | First Coat Finish Paint | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 30 |
| LL1-Z3-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 29-Sep-14 | 01-Oct-14 | 30 |
| LL1-Z2-8200 | First Coat Finish Paint | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 24 |
| L1K-8200 | First Coat Finish Paint | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 11 |
| LL1-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 10-Oct-14 | 14-Oct-14 | 30 |
| LL1-8201 | Final Coat Finish Paint | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 30 |
| LL1-Z2-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 24 |
| LL1-Z3-8201 | Final Coat Finish Paint | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 29 |
| L1K-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 11 |
| LL1-Z2-8201 | Final Coat Finish Paint | 5 | 5 | 23-Oct-14 | 29-Oct-14 | 24 |
| L1B-8200 | First Coat Finish Paint | 5 | 5 | 24-Oct-14 | 30-Oct-14 | 8 |
| LL1-8210 | Owner Walk / Create Punchlist | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 30 |
| LL1-8212 | Resolve Final Punchlist | 5 | 5 | 30-Oct-14 | 05-Nov-14 | 30 |
| LL1-Z3-8210 | Owner Walk / Create Punchlist | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 29 |
| LL1-Z3-8212 | Resolve Final Punchlist | 3 | 3 | 04-Nov-14 | 06-Nov-14 | 29 |
| LL1-8214 | LL1, Zone 1 Complete | 0 | 0 | | 05-Nov-14 | 30 |
| LL1-Z2-8210 | Owner Walk / Create Punchlist | 1 | 1 | 06-Nov-14 | 06-Nov-14 | 24 |
| LL1-Z3-8214 | LL1, Zone 3 Complete | 0 | 0 | | 06-Nov-14 | 29 |
| LL1-Z2-8212 | Resolve Final Punchlist | 5 | 5 | 07-Nov-14 | 14-Nov-14 | 24 |
| L1L-8200 | First Coat Finish Paint | 5 | 5 | 11-Nov-14 | 17-Nov-14 | 0 |
| L1K-8201 | Final Coat Finish Paint | 4 | 4 | 11-Nov-14 | 14-Nov-14 | 9 |
| L1B-8204 | Mech Trim / Finish (HVAC & Plumbing) | 4 | 4 | 12-Nov-14 | 17-Nov-14 | 8 |
| LL1-Z2-8214 | LL1 Zone 2 Compllete | 0 | 0 | | 14-Nov-14 | 24 |
| L1B-8201 | Final Coat Finish Paint | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 8 |

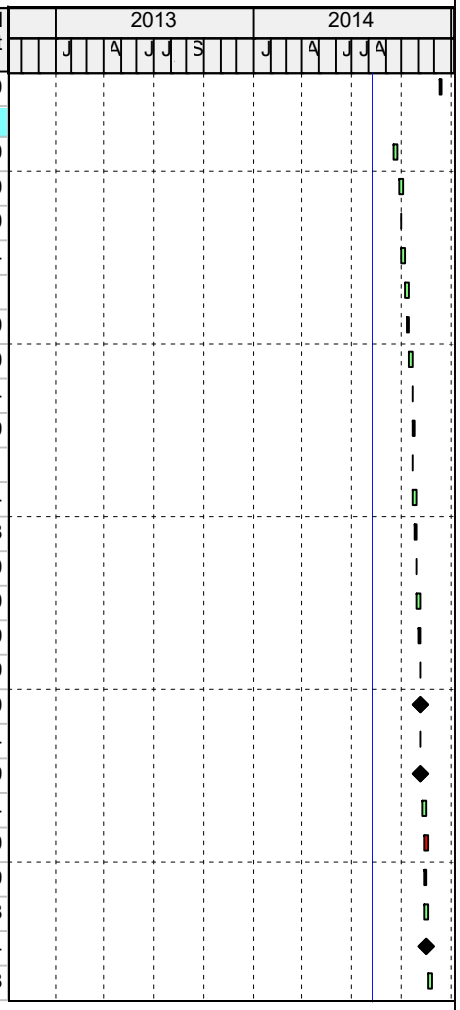


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8210 | Owner Walk / Create Punchlist | 1 | 1 | 24-Nov-14 | 24-Nov-14 | 14 |
| L1K-8212 | Resolve Final Punchlist | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 14 |
| L1L-8204 | Mech Trim / Finish (HVAC & Plumbing) | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 0 |
| L1B-8210 | Owner Walk / Create Punchlist | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 8 |
| L1L-8201 | Final Coat Finish Paint | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 0 |
| L1B-8212 | Resolve Final Punchlist | 5 | 5 | 04-Dec-14 | 10-Dec-14 | 8 |
| L1K-8214 | L1, Zone 1 Complete | 0 | 0 | | 09-Dec-14 | 9 |
| L1B-8214 | L1, Zone 2 Complete | 0 | 0 | | 10-Dec-14 | 8 |
| L1L-8210 | Owner Walk / Create Punchlist | 1 | 1 | 16-Dec-14 | 16-Dec-14 | 0 |
| L1L-8212 | Resolve Final Punchlist | 4 | 4 | 17-Dec-14 | 22-Dec-14 | 0 |
| L1L-8214 | L1, Zone 4 Complete | 0 | 0 | | 22-Dec-14 | 0 |
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8100 | L2 - Insulation | 4 | 4 | 20-Aug-14 | 25-Aug-14 | 33 |
| L02-8102 | L2 - GWB Hang / Tape / Finish - (Including Common / | 12 | 12 | 21-Aug-14 | 04-Sep-14 | 40 |
| L02-8104 | L2 - Int Painting | 2 | 2 | 05-Sep-14 | 08-Sep-14 | 33 |
| L02-8108 | L2 - Elec Trim / Finish | 10 | 10 | 09-Sep-14 | 22-Sep-14 | 36 |
| L02-8110 | L2 - HVAC Trim / Finish | 10 | 10 | 09-Sep-14 | 22-Sep-14 | 36 |
| L02-8112 | L2 - Fire Sprinkler Trim / Finish | 8 | 8 | 09-Sep-14 | 18-Sep-14 | 38 |
| L02-8106 | L2 - Wallcoverings | 6 | 6 | 09-Sep-14 | 16-Sep-14 | 40 |
| L02-8118 | L2 - Elec Specialties Trim / Finish | 10 | 10 | 09-Sep-14 | 22-Sep-14 | 36 |
| L02-8136 | L2 - Lockers / Benches @ Locker Rooms | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 47 |
| L02-8116 | L2 - Finish Carpentry / Millwork | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 33 |
| L02-8120 | L2 - Ceramic Tile / Counter Tops | 8 | 8 | 16-Sep-14 | 25-Sep-14 | 33 |
| L02-8122 | L2 - Plumbing Trim / Finish | 8 | 8 | 18-Sep-14 | 29-Sep-14 | 35 |
| L02-8124 | L2 - Flooring | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 33 |
| L02-8126 | L2 - Doors & Hardware | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 33 |

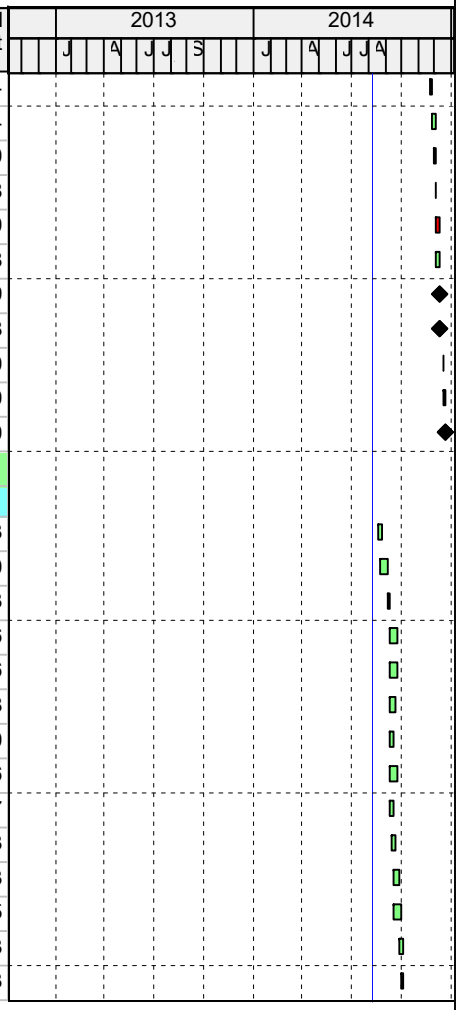



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8128 | L2 - Bath Specialties | 2 | 2 | 30-Sep-14 | 01-Oct-14 | 35 |
| L02-8130 | L2 - Admin / Employee Rooms Substantially Complet | 0 | 0 | | 03-Oct-14 | 33 |
| L02-8132 | L2 - Punch | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 37 |
| L02-8134 | L2 - Clean | 2 | 2 | 13-Oct-14 | 14-Oct-14 | 37 |
| **Corridors** | | | | | | |
| L02-8200 | L2 - Final Paint @ Common / Public Areas | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 33 |
| L02-8114 | L2 - Signage | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 50 |
| L02-8202 | L2 - Elec Trim / Finish @ Common / Public Areas | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 44 |
| L02-8204 | L2 - Mech Trim / Finish @ Common / Public Areas (H | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 33 |
| L02-8206 | L2 - Flooring @ Corridors | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 43 |
| L02-8210 | L2 - Owner Walk / Create Punchlist | 1 | 1 | 20-Oct-14 | 20-Oct-14 | 37 |
| L02-8212 | L2 - Resolve Final Punchlist | 5 | 5 | 21-Oct-14 | 27-Oct-14 | 37 |
| L02-8214 | L2 - Floor Complete | 0 | 0 | | 27-Oct-14 | 37 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L05-8104 | Paint (Prime) | 2 | 1 | 06-Aug-11 A | 08-Aug-14 | 23 |
| L03-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L04-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L05-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L06-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L07-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L08-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L09-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L10-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L11-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L12-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |

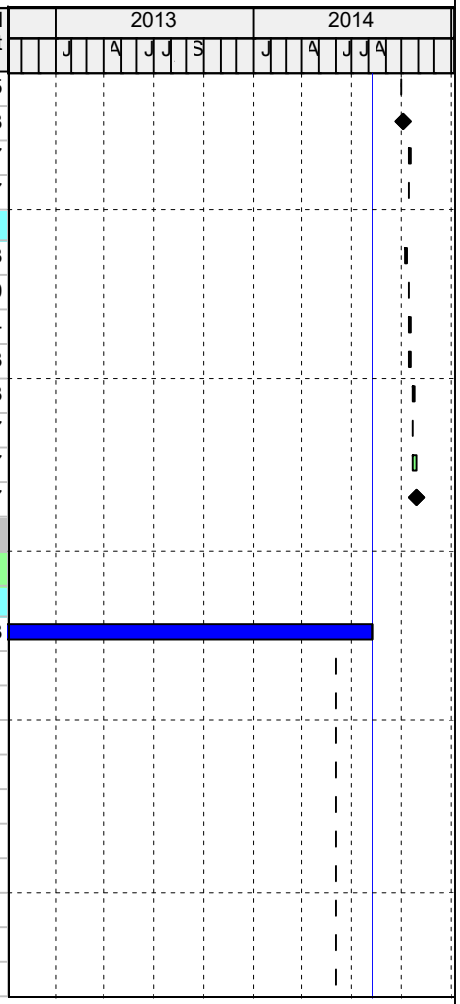



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L15-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L16-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L17-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L03-8102S | Stock GWB | 2 | 0 | 27-Jun-14 A | 08-Jul-14 A | |
| L04-8102 | Hang GWB & Inspection | 4 | 0 | 07-Jul-14 A | 16-Jul-14 A | |
| L04-8102S | Stock GWB | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-8102 | Hang GWB & Inspection | 5 | 0 | 09-Jul-14 A | 22-Jul-14 A | |
| L05-8102S | Stock GWB | 2 | 0 | 10-Jul-14 A | 14-Jul-14 A | |
| L05-8102 | Hang GWB & Inspection | 4 | 0 | 17-Jul-14 A | 23-Jul-14 A | |
| L06-8102S | Stock GWB | 2 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L04-8104 | Paint (Prime) | 2 | 0 | 28-Jul-14 A | 05-Aug-14 A | |
| L03-8104 | Paint (Prime) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L03-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L07-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L08-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L06-8102 | Hang GWB & Inspection | 5 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L07-8102 | Hang GWB & Inspection | 6 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L08-8102 | Hang GWB & Inspection | 6 | 6 | 31-Jul-14 A | 14-Aug-14 | 23 |
| L04-8105 | Paint (First Coat & Ceilings) | 5 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L09-8102S | Stock GWB | 2 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-8105 | Paint (First Coat & Ceilings) | 2 | 2 | 07-Aug-14 A | 11-Aug-14 | 23 |
| L09-8102 | Hang GWB & Inspection | 5 | 4 | 07-Aug-14 A | 12-Aug-14 | 28 |
| L03-8128 | Install Shower/Tub Surrounds | 4 | 4 | 11-Aug-14 | 14-Aug-14 | 21 |
| L06-8104 | Paint (Prime) | 2 | 2 | 12-Aug-14 | 13-Aug-14 | 23 |
| L10-8102S | Stock GWB | 1 | 1 | 12-Aug-14 | 12-Aug-14 | 22 |
| L10-8102 | Hang GWB & Inspection | 4 | 4 | 13-Aug-14 | 16-Aug-14 | 26 |

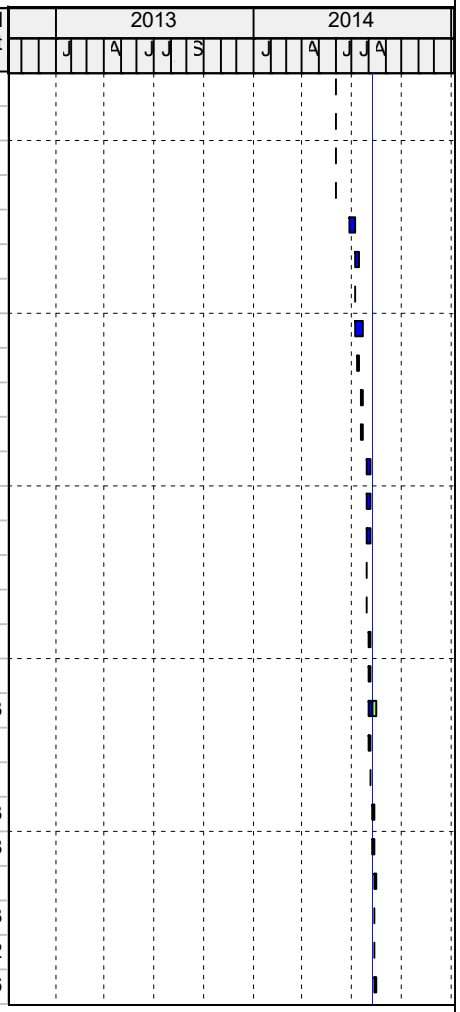



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8128 | Install Shower/Tub Surrounds | 4 | 4 | 14-Aug-14 | 19-Aug-14 | 21 |
| L06-8105 | Paint (First Coat & Ceilings) | 2 | 2 | 14-Aug-14 | 15-Aug-14 | 23 |
| L11-8102S | Stock GWB | 1 | 1 | 15-Aug-14 | 15-Aug-14 | 22 |
| L11-8102 | Hang GWB & Inspection | 4 | 4 | 18-Aug-14 | 21-Aug-14 | 26 |
| L07-8104 | Paint (Prime) | 2 | 2 | 19-Aug-14 | 20-Aug-14 | 20 |
| L05-8128 | Install Shower/Tub Surrounds | 4 | 4 | 20-Aug-14 | 23-Aug-14 | 25 |
| L09-8104 | Paint (Prime) | 2 | 2 | 20-Aug-14 | 21-Aug-14 | 23 |
| L03-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 63 |
| L04-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 58 |
| L07-8105 | Paint (First Coat & Ceilings) | 2 | 2 | 21-Aug-14 | 22-Aug-14 | 20 |
| L12-8102S | Stock GWB | 1 | 1 | 21-Aug-14 | 21-Aug-14 | 22 |
| L05-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 22-Aug-14 | 25-Aug-14 | 62 |
| L08-8104 | Paint (Prime) | 2 | 2 | 22-Aug-14 | 25-Aug-14 | 19 |
| L09-8105 | Paint (First Coat & Ceilings) | 2 | 2 | 22-Aug-14 | 25-Aug-14 | 23 |
| L12-8102 | Hang GWB & Inspection | 4 | 4 | 22-Aug-14 | 26-Aug-14 | 27 |
| L03-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 25-Aug-14 | 28-Aug-14 | 32 |
| L03-8108 | Elec Trim / Finish | 4 | 4 | 25-Aug-14 | 28-Aug-14 | 14 |
| L03-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 25-Aug-14 | 28-Aug-14 | 14 |
| L03-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 25-Aug-14 | 28-Aug-14 | 14 |
| L03-8120 | Install Countertops/Sills | 2 | 2 | 25-Aug-14 | 26-Aug-14 | 14 |
| L04-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 25-Aug-14 | 28-Aug-14 | 32 |
| L04-8108 | Elec Trim / Finish | 4 | 4 | 25-Aug-14 | 28-Aug-14 | 14 |
| L04-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 25-Aug-14 | 28-Aug-14 | 14 |
| L04-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 25-Aug-14 | 28-Aug-14 | 14 |
| L06-8128 | Install Shower/Tub Surrounds | 4 | 4 | 25-Aug-14 | 28-Aug-14 | 21 |
| L10-8104 | Paint (Prime) | 2 | 2 | 25-Aug-14 | 26-Aug-14 | 23 |
| L05-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 26-Aug-14 | 29-Aug-14 | 32 |

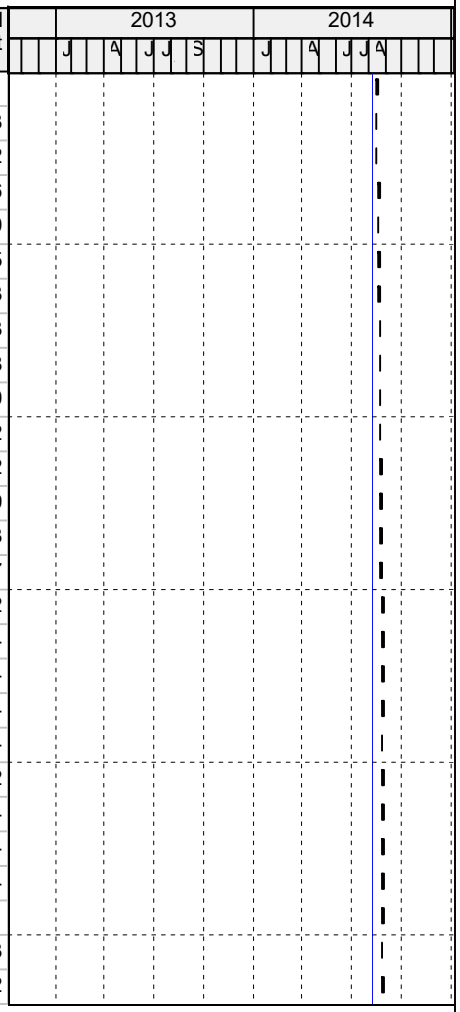



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8108 | Elec Trim / Finish | 4 | 4 | 26-Aug-14 | 29-Aug-14 | 14 |
| L05-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 26-Aug-14 | 29-Aug-14 | 14 |
| L05-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 26-Aug-14 | 29-Aug-14 | 14 |
| L08-8105 | Paint (First Coat & Ceilings) | 2 | 2 | 26-Aug-14 | 27-Aug-14 | 19 |
| L14-8102S | Stock GWB | 1 | 1 | 26-Aug-14 | 26-Aug-14 | 22 |
| L03-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 20 |
| L03-8118 | Low Voltage Trim / Finish | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 61 |
| L04-8120 | Install Countertops/Sills | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 41 |
| L04-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 25 |
| L04-8118 | Low Voltage Trim / Finish | 4 | 4 | 27-Aug-14 | 02-Sep-14 | 50 |
| L06-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 58 |
| L10-8105 | Paint (First Coat & Ceilings) | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 23 |
| L14-8102 | Hang GWB & Inspection | 4 | 4 | 27-Aug-14 | 02-Sep-14 | 22 |
| L03-8116 | Install Base at Guestrooms | 5 | 5 | 28-Aug-14 | 03-Sep-14 | 75 |
| L04-8116 | Install Base at Guestrooms | 5 | 5 | 28-Aug-14 | 03-Sep-14 | 59 |
| L05-8118 | Low Voltage Trim / Finish | 4 | 4 | 28-Aug-14 | 03-Sep-14 | 54 |
| L05-8120 | Install Countertops/Sills | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 41 |
| L06-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 29-Aug-14 | 04-Sep-14 | 32 |
| L06-8108 | Elec Trim / Finish | 4 | 4 | 29-Aug-14 | 04-Sep-14 | 14 |
| L06-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 29-Aug-14 | 04-Sep-14 | 14 |
| L06-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 29-Aug-14 | 04-Sep-14 | 14 |
| L07-8128 | Install Shower/Tub Surrounds | 4 | 4 | 29-Aug-14 | 04-Sep-14 | 21 |
| L07-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 56 |
| L11-8104 | Paint (Prime) | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 23 |
| L03-8107 | Paint Final Coat | 3 | 3 | 02-Sep-14 | 04-Sep-14 | 61 |
| L06-8118 | Low Voltage Trim / Finish | 4 | 4 | 02-Sep-14 | 05-Sep-14 | 50 |
| L10-8128 | Install Shower/Tub Surrounds | 4 | 4 | 02-Sep-14 | 05-Sep-14 | 33 |

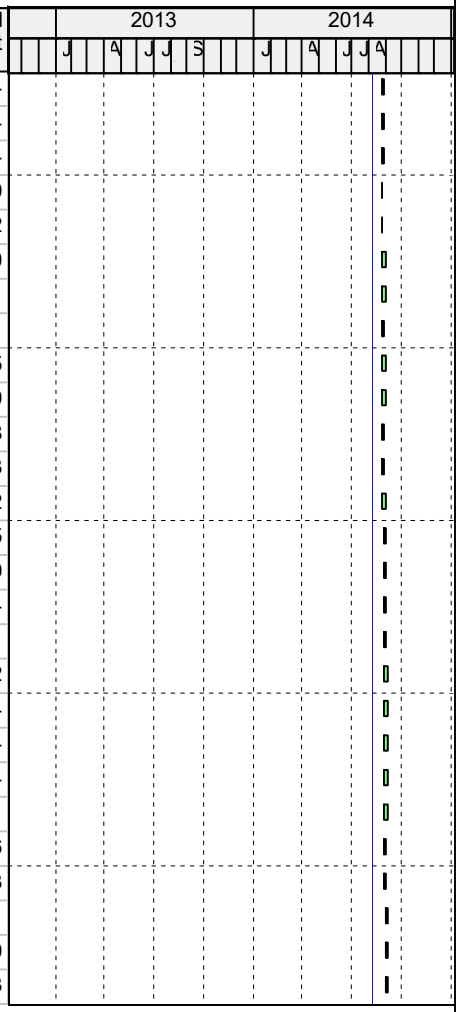



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8102S | Stock GWB | 1 | 1 | 02-Sep-14 | 02-Sep-14 | 22 |
| L05-8107 | Paint Final Coat | 3 | 3 | 03-Sep-14 | 05-Sep-14 | 54 |
| L06-8120 | Install Countertops/Sills | 2 | 2 | 03-Sep-14 | 04-Sep-14 | 41 |
| L07-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 03-Sep-14 | 08-Sep-14 | 32 |
| L07-8108 | Elec Trim / Finish | 4 | 4 | 03-Sep-14 | 08-Sep-14 | 14 |
| L07-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 03-Sep-14 | 08-Sep-14 | 14 |
| L07-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 03-Sep-14 | 08-Sep-14 | 14 |
| L08-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 03-Sep-14 | 04-Sep-14 | 59 |
| L11-8105 | Paint (First Coat & Ceilings) | 2 | 2 | 03-Sep-14 | 04-Sep-14 | 23 |
| L15-8102 | Hang GWB & Inspection | 5 | 5 | 03-Sep-14 | 08-Sep-14 | 26 |
| L04-8107 | Paint Final Coat | 3 | 3 | 04-Sep-14 | 08-Sep-14 | 48 |
| L05-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 20 |
| L06-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 04-Sep-14 | 10-Sep-14 | 25 |
| L09-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 04-Sep-14 | 05-Sep-14 | 59 |
| L03-8114 | Signage (By Owner) | 5 | 5 | 05-Sep-14 | 11-Sep-14 | 61 |
| L05-8116 | Install Base at Guestrooms | 5 | 5 | 05-Sep-14 | 11-Sep-14 | 56 |
| L06-8116 | Install Base at Guestrooms | 5 | 5 | 05-Sep-14 | 11-Sep-14 | 56 |
| L07-8120 | Install Countertops/Sills | 2 | 2 | 05-Sep-14 | 08-Sep-14 | 41 |
| L08-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 05-Sep-14 | 10-Sep-14 | 32 |
| L08-8108 | Elec Trim / Finish | 4 | 4 | 05-Sep-14 | 10-Sep-14 | 14 |
| L08-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 05-Sep-14 | 10-Sep-14 | 14 |
| L08-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 05-Sep-14 | 10-Sep-14 | 14 |
| L08-8128 | Install Shower/Tub Surrounds | 4 | 4 | 05-Sep-14 | 10-Sep-14 | 21 |
| L12-8104 | Paint (Prime) | 2 | 2 | 05-Sep-14 | 08-Sep-14 | 23 |
| L16-8102S | Stock GWB | 1 | 1 | 05-Sep-14 | 05-Sep-14 | 22 |
| L05-8114 | Signage (By Owner) | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 60 |
| L06-8107 | Paint Final Coat | 3 | 3 | 08-Sep-14 | 10-Sep-14 | 50 |

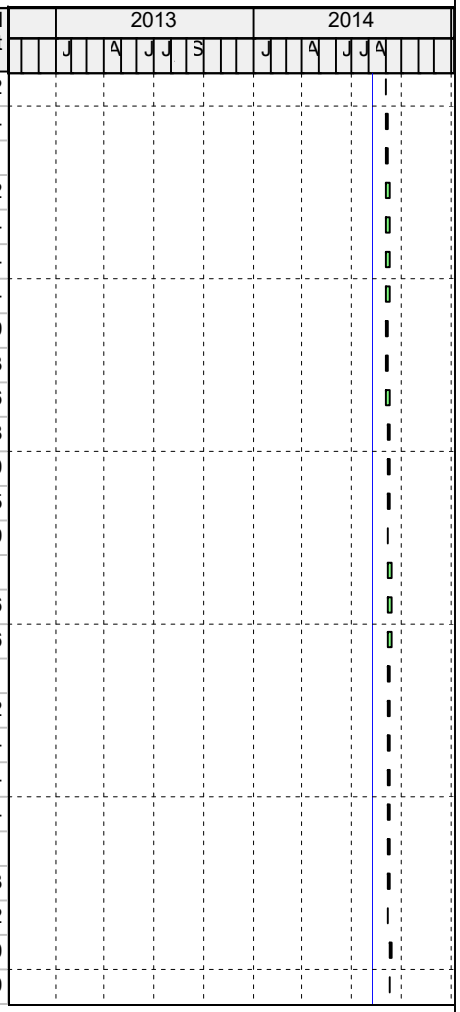



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8118 | Low Voltage Trim / Finish | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 51 |
| L11-8128 | Install Shower/Tub Surrounds | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 33 |
| L16-8102 | Hang GWB & Inspection | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 26 |
| L04-8114 | Signage (By Owner) | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 59 |
| L07-8118 | Low Voltage Trim / Finish | 4 | 4 | 09-Sep-14 | 12-Sep-14 | 45 |
| L08-8120 | Install Countertops/Sills | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 41 |
| L09-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 09-Sep-14 | 12-Sep-14 | 32 |
| L09-8108 | Elec Trim / Finish | 4 | 4 | 09-Sep-14 | 12-Sep-14 | 14 |
| L09-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 09-Sep-14 | 12-Sep-14 | 14 |
| L09-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 09-Sep-14 | 12-Sep-14 | 14 |
| L09-8118 | Low Voltage Trim / Finish | 4 | 4 | 09-Sep-14 | 12-Sep-14 | 51 |
| L10-8109 | Acoustical Ceiling Tile @ Corridors | 3 | 3 | 09-Sep-14 | 11-Sep-14 | 54 |
| L12-8105 | Paint (First Coat & Ceilings) | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 23 |
| L03-8126 | Doors & Hardware | 5 | 5 | 10-Sep-14 | 15-Sep-14 | 21 |
| L14-8104 | Paint (Prime) | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 23 |
| L06-8114 | Signage (By Owner) | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 57 |
| L07-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 20 |
| L08-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 25 |
| L09-8120 | Install Countertops/Sills | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 41 |
| L09-8128 | Install Shower/Tub Surrounds | 4 | 4 | 11-Sep-14 | 16-Sep-14 | 21 |
| L17-8102S | Stock GWB | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 21 |
| L07-8116 | Install Base at Guestrooms | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 51 |
| L08-8116 | Install Base at Guestrooms | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 51 |
| L08-8107 | Paint Final Coat | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 51 |
| L10-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 12-Sep-14 | 17-Sep-14 | 32 |
| L10-8108 | Elec Trim / Finish | 4 | 4 | 12-Sep-14 | 17-Sep-14 | 14 |
| L10-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 12-Sep-14 | 17-Sep-14 | 14 |

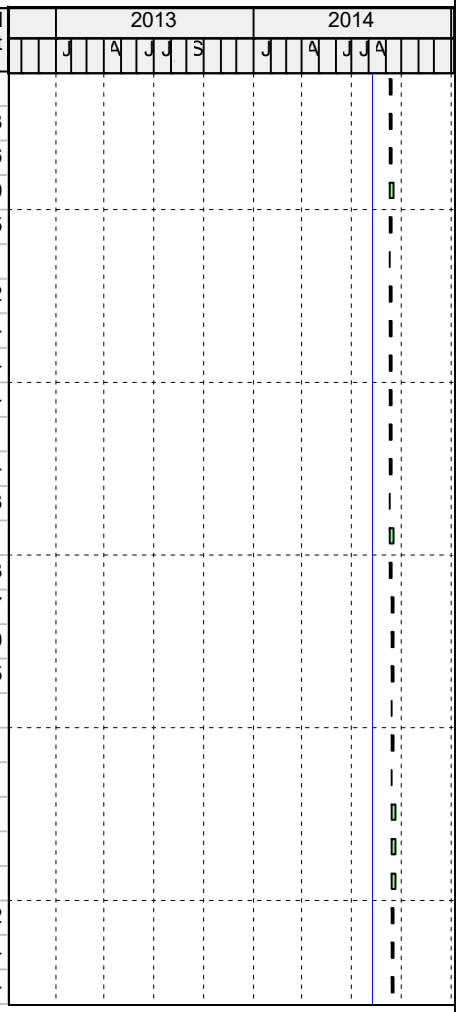


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 12-Sep-14 | 17-Sep-14 | 14 |
| L12-8128 | Install Shower/Tub Surrounds | 4 | 4 | 12-Sep-14 | 17-Sep-14 | 33 |
| L14-8105 | Paint (First Coat & Ceilings) | 2 | 2 | 12-Sep-14 | 15-Sep-14 | 23 |
| L17-8102 | Hang GWB & Inspection | 4 | 4 | 12-Sep-14 | 16-Sep-14 | 26 |
| L04-8126 | Doors & Hardware | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 21 |
| L07-8107 | Paint Final Coat | 3 | 3 | 15-Sep-14 | 17-Sep-14 | 45 |
| L09-8107 | Paint Final Coat | 3 | 3 | 15-Sep-14 | 17-Sep-14 | 51 |
| L10-8120 | Install Countertops/Sills | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 41 |
| L10-8118 | Low Voltage Trim / Finish | 4 | 4 | 15-Sep-14 | 18-Sep-14 | 48 |
| L11-8109 | Acoustical Ceiling Tile @ Corridors | 3 | 3 | 15-Sep-14 | 17-Sep-14 | 29 |
| L15-8104 | Paint (Prime) | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 23 |
| L05-8132 | Punchlist @ Guestrooms | 5 | 5 | 16-Sep-14 | 22-Sep-14 | 54 |
| L05-8134 | Final Clean @ Guestrooms | 5 | 5 | 16-Sep-14 | 22-Sep-14 | 54 |
| L11-8120 | Install Countertops/Sills | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 41 |
| L15-8105 | Paint (First Coat & Ceilings) | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 23 |
| L04-8132 | Punchlist @ Guestrooms | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 52 |
| L04-8134 | Final Clean @ Guestrooms | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 52 |
| L07-8114 | Signage (By Owner) | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 47 |
| L09-8114 | Signage (By Owner) | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 52 |
| L09-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 20 |
| L10-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 25 |
| L11-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 18-Sep-14 | 23-Sep-14 | 32 |
| L11-8108 | Elec Trim / Finish | 4 | 4 | 18-Sep-14 | 23-Sep-14 | 14 |
| L11-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 18-Sep-14 | 23-Sep-14 | 14 |
| L11-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 18-Sep-14 | 23-Sep-14 | 14 |
| L14-8128 | Install Shower/Tub Surrounds | 4 | 4 | 18-Sep-14 | 23-Sep-14 | 33 |
| L16-8104 | Paint (Prime) | 2 | 2 | 18-Sep-14 | 19-Sep-14 | 22 |

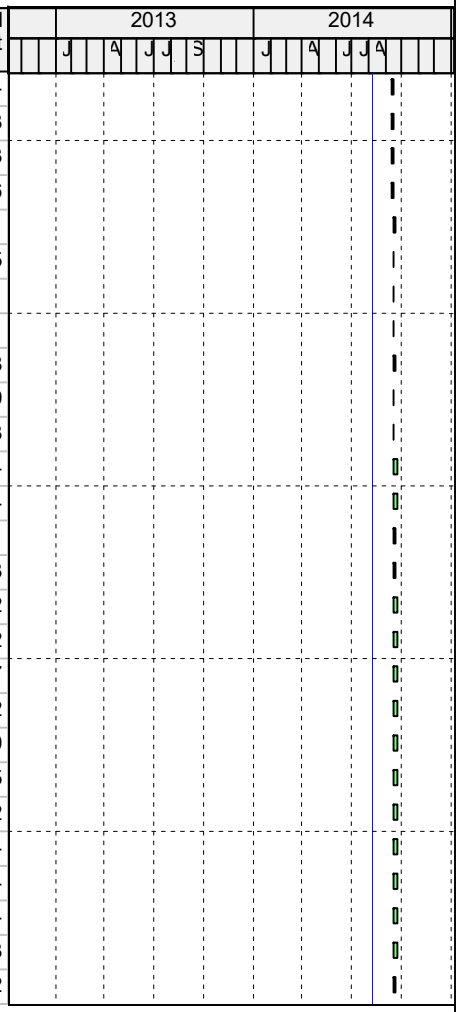



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8126 | Doors & Hardware | 5 | 5 | 19-Sep-14 | 24-Sep-14 | 21 |
| L08-8114 | Signage (By Owner) | 5 | 5 | 19-Sep-14 | 25-Sep-14 | 51 |
| L09-8116 | Install Base at Guestrooms | 5 | 5 | 19-Sep-14 | 25-Sep-14 | 46 |
| L10-8116 | Install Base at Guestrooms | 5 | 5 | 19-Sep-14 | 25-Sep-14 | 46 |
| L10-8107 | Paint Final Coat | 3 | 3 | 19-Sep-14 | 23-Sep-14 | 48 |
| L12-8120 | Install Countertops/Sills | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 41 |
| L12-8109 | Acoustical Ceiling Tile @ Corridors | 3 | 3 | 19-Sep-14 | 23-Sep-14 | 31 |
| L08-8132 | Punchlist @ Guestrooms | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 50 |
| L08-8134 | Final Clean @ Guestrooms | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 50 |
| L11-8118 | Low Voltage Trim / Finish | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 20 |
| L16-8105 | Paint (First Coat & Ceilings) | 2 | 2 | 22-Sep-14 | 23-Sep-14 | 22 |
| L14-8120 | Install Countertops/Sills | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 41 |
| L06-8126 | Doors & Hardware | 5 | 5 | 24-Sep-14 | 29-Sep-14 | 21 |
| L06-8132 | Punchlist @ Guestrooms | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 48 |
| L06-8134 | Final Clean @ Guestrooms | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 48 |
| L10-8114 | Signage (By Owner) | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 48 |
| L12-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 24-Sep-14 | 29-Sep-14 | 32 |
| L12-8108 | Elec Trim / Finish | 4 | 4 | 24-Sep-14 | 29-Sep-14 | 14 |
| L12-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 24-Sep-14 | 29-Sep-14 | 14 |
| L12-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 24-Sep-14 | 29-Sep-14 | 14 |
| L14-8109 | Acoustical Ceiling Tile @ Corridors | 3 | 3 | 24-Sep-14 | 26-Sep-14 | 32 |
| L15-8128 | Install Shower/Tub Surrounds | 4 | 4 | 24-Sep-14 | 29-Sep-14 | 33 |
| L11-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 20 |
| L12-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 25 |
| L17-8104 | Paint (Prime) | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 21 |
| L09-8132 | Punchlist @ Guestrooms | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 46 |
| L09-8134 | Final Clean @ Guestrooms | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 46 |

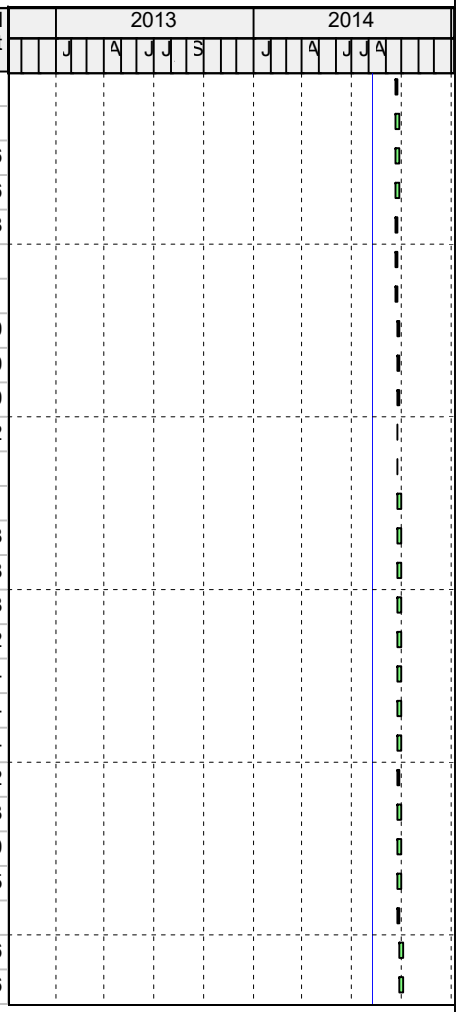



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8132 | Punchlist @ Guestrooms | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 46 |
| L10-8134 | Final Clean @ Guestrooms | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 46 |
| L11-8116 | Install Base at Guestrooms | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 41 |
| L11-8107 | Paint Final Coat | 3 | 3 | 26-Sep-14 | 30-Sep-14 | 20 |
| L12-8116 | Install Base at Guestrooms | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 41 |
| L12-8118 | Low Voltage Trim / Finish | 4 | 4 | 26-Sep-14 | 01-Oct-14 | 39 |
| L15-8120 | Install Countertops/Sills | 2 | 2 | 26-Sep-14 | 29-Sep-14 | 40 |
| L07-8126 | Doors & Hardware | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 21 |
| L07-8132 | Punchlist @ Guestrooms | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 45 |
| L07-8134 | Final Clean @ Guestrooms | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 45 |
| L14-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 29-Sep-14 | 02-Oct-14 | 32 |
| L14-8108 | Elec Trim / Finish | 4 | 4 | 29-Sep-14 | 02-Oct-14 | 14 |
| L14-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 29-Sep-14 | 02-Oct-14 | 14 |
| L14-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 29-Sep-14 | 02-Oct-14 | 14 |
| L15-8109 | Acoustical Ceiling Tile @ Corridors | 3 | 3 | 29-Sep-14 | 01-Oct-14 | 34 |
| L17-8105 | Paint (First Coat & Ceilings) | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 21 |
| L16-8128 | Install Shower/Tub Surrounds | 4 | 4 | 30-Sep-14 | 03-Oct-14 | 33 |
| L11-8114 | Signage (By Owner) | 5 | 5 | 01-Oct-14 | 07-Oct-14 | 43 |
| L14-8118 | Low Voltage Trim / Finish | 4 | 4 | 01-Oct-14 | 06-Oct-14 | 36 |
| L16-8120 | Install Countertops/Sills | 2 | 2 | 01-Oct-14 | 02-Oct-14 | 39 |
| L12-8107 | Paint Final Coat | 3 | 3 | 02-Oct-14 | 06-Oct-14 | 39 |
| L14-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 02-Oct-14 | 08-Oct-14 | 24 |
| L15-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 02-Oct-14 | 07-Oct-14 | 32 |
| L15-8108 | Elec Trim / Finish | 4 | 4 | 02-Oct-14 | 07-Oct-14 | 14 |
| L15-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 02-Oct-14 | 07-Oct-14 | 14 |
| L15-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 02-Oct-14 | 07-Oct-14 | 14 |
| L15-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 02-Oct-14 | 08-Oct-14 | 29 |

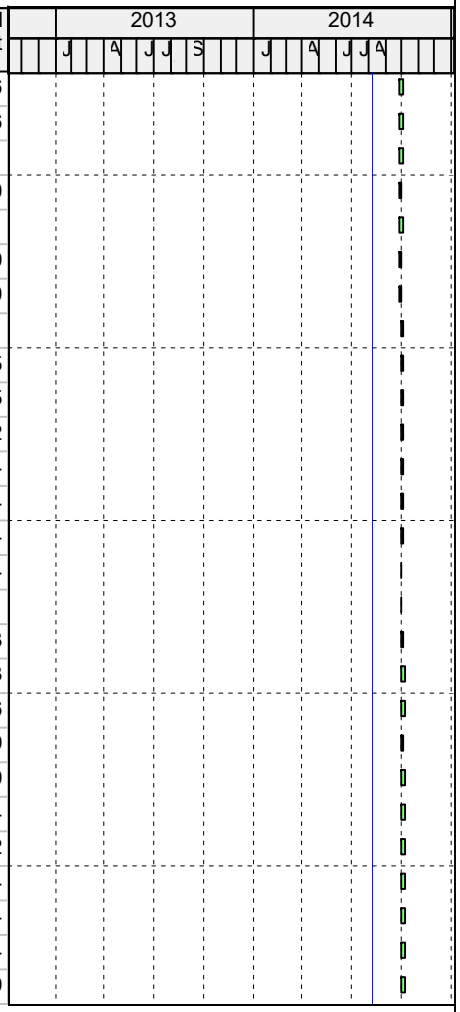



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 02-Oct-14 | 03-Oct-14 | 33 |
| L11-8132 | Punchlist @ Guestrooms | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 41 |
| L11-8134 | Final Clean @ Guestrooms | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 41 |
| L14-8116 | Install Base at Guestrooms | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 36 |
| L15-8116 | Install Base at Guestrooms | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 36 |
| L08-8126 | Doors & Hardware | 5 | 5 | 04-Oct-14 | 09-Oct-14 | 21 |
| L15-8118 | Low Voltage Trim / Finish | 4 | 4 | 06-Oct-14 | 09-Oct-14 | 33 |
| L16-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 06-Oct-14 | 09-Oct-14 | 32 |
| L16-8108 | Elec Trim / Finish | 4 | 4 | 06-Oct-14 | 09-Oct-14 | 14 |
| L16-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 06-Oct-14 | 09-Oct-14 | 14 |
| L16-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 06-Oct-14 | 09-Oct-14 | 14 |
| L17-8128 | Install Shower/Tub Surrounds | 4 | 4 | 06-Oct-14 | 09-Oct-14 | 33 |
| L03-8132 | Punchlist @ Guestrooms | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 39 |
| L03-8134 | Final Clean @ Guestrooms | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 39 |
| L12-8114 | Signage (By Owner) | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 39 |
| L14-8107 | Paint Final Coat | 3 | 3 | 07-Oct-14 | 09-Oct-14 | 36 |
| L16-8118 | Low Voltage Trim / Finish | 4 | 4 | 08-Oct-14 | 13-Oct-14 | 31 |
| L17-8120 | Install Countertops/Sills | 2 | 2 | 08-Oct-14 | 09-Oct-14 | 36 |
| L09-8126 | Doors & Hardware | 5 | 5 | 09-Oct-14 | 14-Oct-14 | 21 |
| L16-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 25 |
| L17-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 30 |
| L17-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 09-Oct-14 | 10-Oct-14 | 33 |
| L12-8132 | Punchlist @ Guestrooms | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 36 |
| L12-8134 | Final Clean @ Guestrooms | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 36 |
| L14-8114 | Signage (By Owner) | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 36 |
| L15-8107 | Paint Final Coat | 3 | 3 | 10-Oct-14 | 14-Oct-14 | 33 |
| L16-8116 | Install Base at Guestrooms | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 32 |

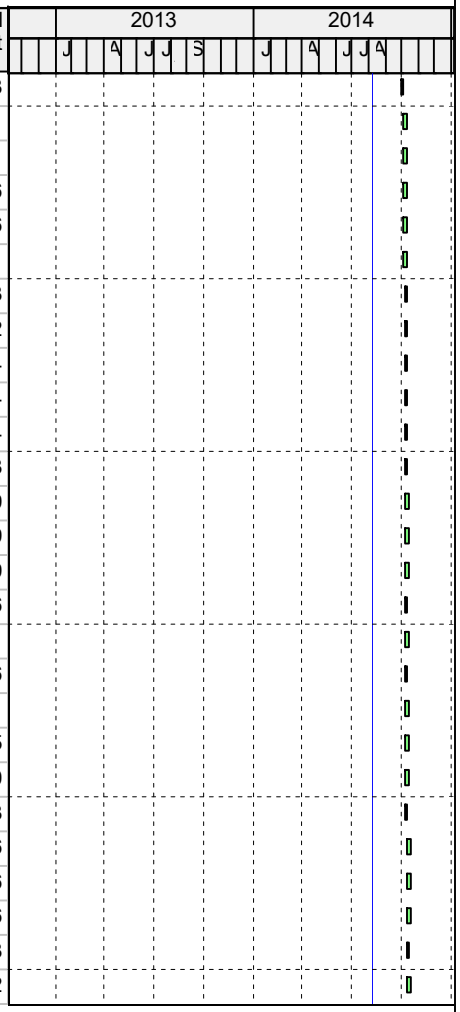



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 10-Oct-14 | 15-Oct-14 | 32 |
| L17-8108 | Elec Trim / Finish | 4 | 4 | 10-Oct-14 | 15-Oct-14 | 14 |
| L17-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 10-Oct-14 | 15-Oct-14 | 14 |
| L17-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 10-Oct-14 | 15-Oct-14 | 14 |
| L17-8116 | Install Base at Guestrooms | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 31 |
| L10-8126 | Doors & Hardware | 5 | 5 | 14-Oct-14 | 18-Oct-14 | 21 |
| L17-8118 | Low Voltage Trim / Finish | 4 | 4 | 14-Oct-14 | 17-Oct-14 | 28 |
| L15-8114 | Signage (By Owner) | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 33 |
| L16-8107 | Paint Final Coat | 3 | 3 | 15-Oct-14 | 17-Oct-14 | 30 |
| L14-8132 | Punchlist @ Guestrooms | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 31 |
| L14-8134 | Final Clean @ Guestrooms | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 31 |
| L11-8126 | Doors & Hardware | 5 | 5 | 18-Oct-14 | 23-Oct-14 | 21 |
| L16-8114 | Signage (By Owner) | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 30 |
| L17-8107 | Paint Final Coat | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 26 |
| L12-8126 | Doors & Hardware | 5 | 5 | 23-Oct-14 | 28-Oct-14 | 21 |
| L15-8132 | Punchlist @ Guestrooms | 5 | 5 | 24-Oct-14 | 30-Oct-14 | 26 |
| L15-8134 | Final Clean @ Guestrooms | 5 | 5 | 24-Oct-14 | 30-Oct-14 | 26 |
| L17-8114 | Signage (By Owner) | 5 | 5 | 24-Oct-14 | 30-Oct-14 | 26 |
| L14-8126 | Doors & Hardware | 5 | 5 | 28-Oct-14 | 01-Nov-14 | 21 |
| L16-8132 | Punchlist @ Guestrooms | 5 | 5 | 29-Oct-14 | 03-Nov-14 | 29 |
| L16-8134 | Final Clean @ Guestrooms | 5 | 5 | 29-Oct-14 | 03-Nov-14 | 29 |
| L17-8132 | Punchlist @ Guestrooms | 5 | 5 | 31-Oct-14 | 06-Nov-14 | 21 |
| L17-8134 | Final Clean @ Guestrooms | 5 | 5 | 31-Oct-14 | 06-Nov-14 | 21 |
| L15-8126 | Doors & Hardware | 5 | 5 | 01-Nov-14 | 06-Nov-14 | 21 |
| L16-8126 | Doors & Hardware | 5 | 5 | 06-Nov-14 | 11-Nov-14 | 21 |
| L17-8126 | Doors & Hardware | 5 | 5 | 11-Nov-14 | 15-Nov-14 | 21 |
| **Pool Area** | | | | | | |

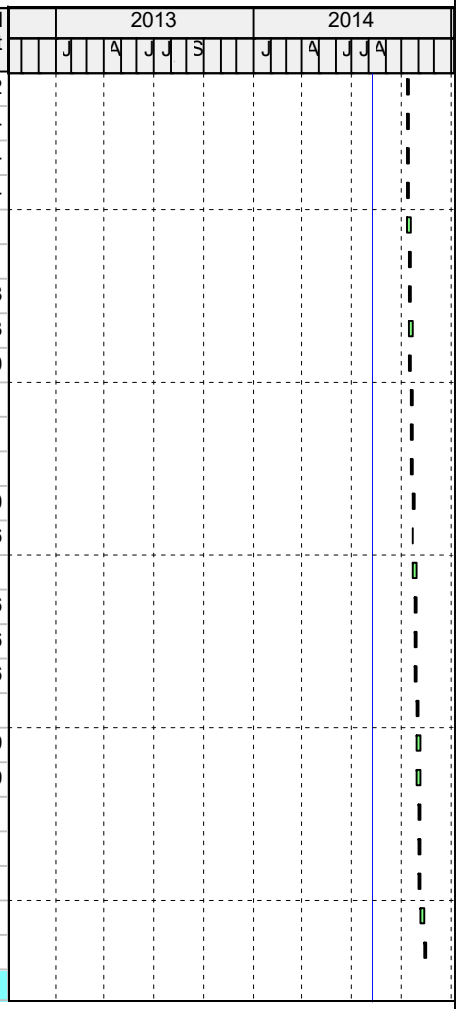



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8216 | Pool - Install tile, coping and depth markers | 10 | 10 | 29-Aug-14 | 12-Sep-14 | 27 |
| L03-8218 | Pool - Install pool equipment | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 27 |
| **Corridors / Common / Public Areas** | | | | | | |
| L03-8200 | Vinyl Wall Coverings | 3 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L04-8200 | Vinyl Wall Coverings | 5 | 3 | 06-Aug-14 A | 12-Aug-14 | 57 |
| L05-8200 | Vinyl Wall Coverings | 5 | 5 | 12-Aug-14 | 18-Aug-14 | 23 |
| L06-8200 | Vinyl Wall Coverings | 5 | 5 | 15-Aug-14 | 21-Aug-14 | 23 |
| L03-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 19-Aug-14 | 20-Aug-14 | 63 |
| L04-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 19-Aug-14 | 20-Aug-14 | 58 |
| L05-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 20-Aug-14 | 21-Aug-14 | 62 |
| L07-8200 | Vinyl Wall Coverings | 5 | 5 | 22-Aug-14 | 28-Aug-14 | 22 |
| L06-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 25-Aug-14 | 26-Aug-14 | 58 |
| L09-8200 | Vinyl Wall Coverings | 5 | 5 | 26-Aug-14 | 02-Sep-14 | 26 |
| L07-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 27-Aug-14 | 28-Aug-14 | 56 |
| L10-8200 | Vinyl Wall Coverings | 5 | 5 | 27-Aug-14 | 03-Sep-14 | 33 |
| L08-8200 | Vinyl Wall Coverings | 5 | 5 | 28-Aug-14 | 04-Sep-14 | 54 |
| L08-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 29-Aug-14 | 02-Sep-14 | 59 |
| L09-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 02-Sep-14 | 03-Sep-14 | 59 |
| L11-8200 | Vinyl Wall Coverings | 5 | 5 | 03-Sep-14 | 09-Sep-14 | 29 |
| L10-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 05-Sep-14 | 08-Sep-14 | 54 |
| L05-8206 | Install Flooring @ Corridors | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 54 |
| L04-8206 | Install Flooring @ Corridors | 4 | 4 | 09-Sep-14 | 12-Sep-14 | 48 |
| L12-8200 | Vinyl Wall Coverings | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 31 |
| L11-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 29 |
| L14-8200 | Vinyl Wall Coverings | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 32 |
| L06-8206 | Install Flooring @ Corridors | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 48 |
| L12-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 31 |

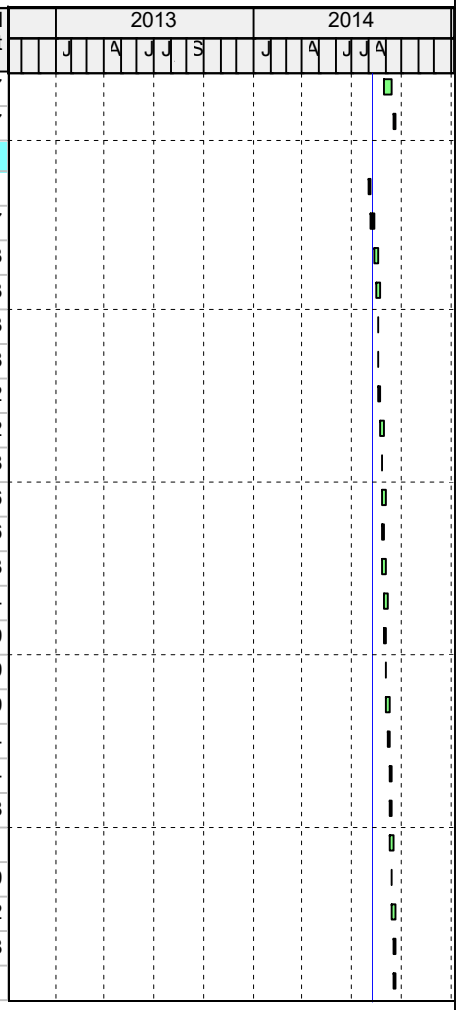


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8200 | Vinyl Wall Coverings | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 34 |
| L07-8206 | Install Flooring @ Corridors | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 45 |
| L08-8206 | Install Flooring @ Corridors | 2 | 2 | 18-Sep-14 | 19-Sep-14 | 50 |
| L14-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 22-Sep-14 | 23-Sep-14 | 32 |
| L16-8200 | Vinyl Wall Coverings | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 33 |
| L05-8208 | Final Clean (Entire Floor) | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 54 |
| L10-8206 | Install Flooring @ Corridors | 3 | 3 | 24-Sep-14 | 26-Sep-14 | 46 |
| L04-8208 | Final Clean (Entire Floor) | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 52 |
| L05-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 25-Sep-14 | 25-Sep-14 | 54 |
| L09-8206 | Install Flooring @ Corridors | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 46 |
| L15-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 34 |
| L05-8212 | Resolve Final Punchlist | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 54 |
| L03-8206 | Install Flooring @ Corridors | 4 | 4 | 27-Sep-14 | 01-Oct-14 | 48 |
| L04-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 29-Sep-14 | 29-Sep-14 | 52 |
| L08-8208 | Final Clean (Entire Floor) | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 50 |
| L17-8200 | Vinyl Wall Coverings | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 33 |
| L04-8212 | Resolve Final Punchlist | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 52 |
| L16-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 30-Sep-14 | 01-Oct-14 | 33 |
| L06-8208 | Final Clean (Entire Floor) | 2 | 2 | 01-Oct-14 | 02-Oct-14 | 48 |
| L11-8206 | Install Flooring @ Corridors | 3 | 3 | 01-Oct-14 | 03-Oct-14 | 20 |
| L05-8214 | Floor Complete | 0 | 0 | | 02-Oct-14 | 54 |
| L06-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 48 |
| L06-8212 | Resolve Final Punchlist | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 48 |
| L07-8208 | Final Clean (Entire Floor) | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 45 |
| L04-8214 | Floor Complete | 0 | 0 | | 06-Oct-14 | 52 |
| L09-8208 | Final Clean (Entire Floor) | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 44 |
| L10-8208 | Final Clean (Entire Floor) | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 44 |

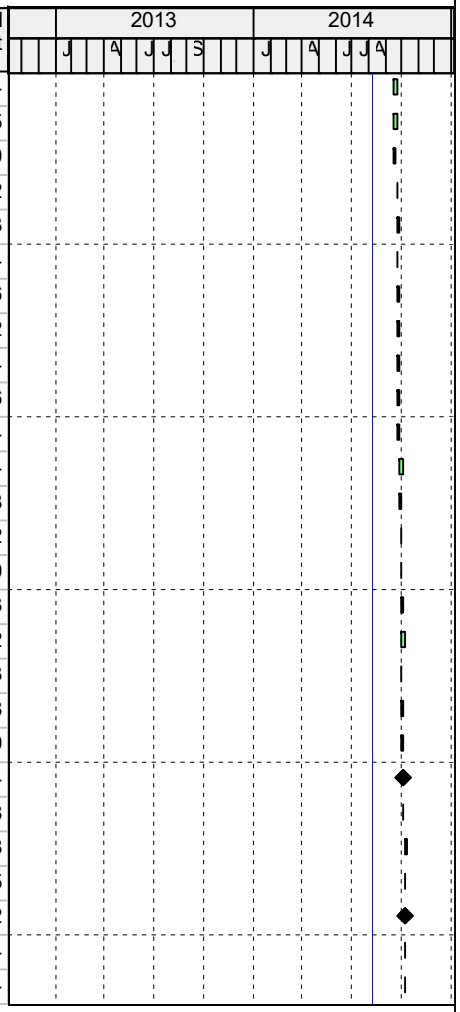


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 33 |
| L07-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 45 |
| L12-8206 | Install Flooring @ Corridors | 4 | 4 | 08-Oct-14 | 11-Oct-14 | 25 |
| L07-8212 | Resolve Final Punchlist | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 45 |
| L08-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 43 |
| L06-8214 | Floor Complete | 0 | 0 | | 10-Oct-14 | 48 |
| L08-8212 | Resolve Final Punchlist | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 43 |
| L09-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 15-Oct-14 | 15-Oct-14 | 40 |
| L11-8208 | Final Clean (Entire Floor) | 2 | 2 | 15-Oct-14 | 16-Oct-14 | 38 |
| L14-8206 | Install Flooring @ Corridors | 4 | 4 | 15-Oct-14 | 18-Oct-14 | 25 |
| L07-8214 | Floor Complete | 0 | 0 | | 15-Oct-14 | 45 |
| L09-8212 | Resolve Final Punchlist | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 40 |
| L12-8208 | Final Clean (Entire Floor) | 2 | 2 | 17-Oct-14 | 20-Oct-14 | 36 |
| L08-8214 | Floor Complete | 0 | 0 | | 17-Oct-14 | 43 |
| L10-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 20-Oct-14 | 20-Oct-14 | 37 |
| L10-8212 | Resolve Final Punchlist | 5 | 5 | 21-Oct-14 | 27-Oct-14 | 37 |
| L15-8206 | Install Flooring @ Corridors | 4 | 4 | 22-Oct-14 | 25-Oct-14 | 25 |
| L09-8214 | Floor Complete | 0 | 0 | | 22-Oct-14 | 40 |
| L16-8206 | Install Flooring @ Corridors | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 20 |
| L11-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 24-Oct-14 | 24-Oct-14 | 33 |
| L14-8208 | Final Clean (Entire Floor) | 2 | 2 | 24-Oct-14 | 27-Oct-14 | 31 |
| L11-8212 | Resolve Final Punchlist | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 33 |
| L10-8214 | Floor Complete | 0 | 0 | | 27-Oct-14 | 37 |
| L12-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 30 |
| L17-8206 | Install Flooring @ Corridors | 4 | 4 | 29-Oct-14 | 01-Nov-14 | 26 |
| L03-8208 | Final Clean (Entire Floor) | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 27 |
| L12-8212 | Resolve Final Punchlist | 5 | 5 | 30-Oct-14 | 05-Nov-14 | 30 |

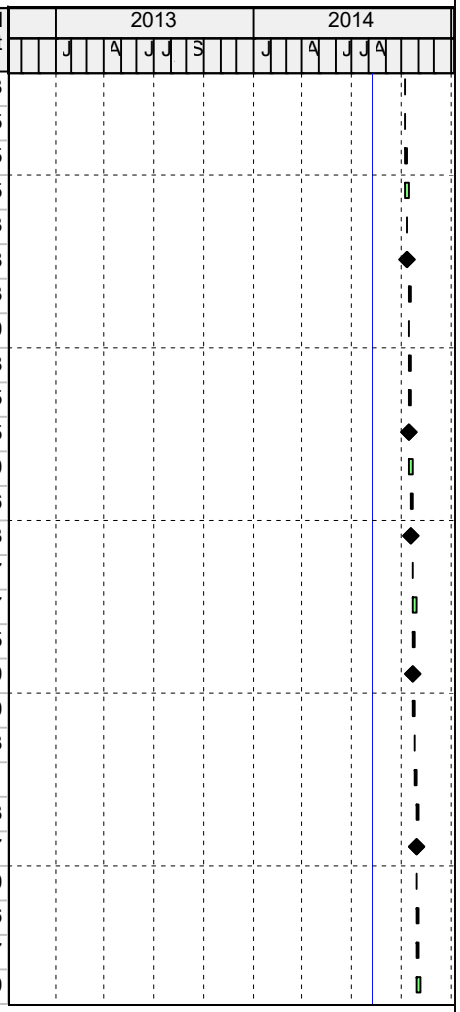


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8208 | Final Clean (Entire Floor) | 2 | 2 | 31-Oct-14 | 03-Nov-14 | 26 |
| L11-8214 | Floor Complete | 0 | 0 | | 31-Oct-14 | 33 |
| L03-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 27 |
| L14-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 27 |
| L03-8212 | Resolve Final Punchlist | 5 | 5 | 04-Nov-14 | 11-Nov-14 | 27 |
| L14-8212 | Resolve Final Punchlist | 5 | 5 | 04-Nov-14 | 11-Nov-14 | 27 |
| L16-8208 | Final Clean (Entire Floor) | 2 | 2 | 04-Nov-14 | 05-Nov-14 | 24 |
| L12-8214 | Floor Complete | 0 | 0 | | 05-Nov-14 | 30 |
| L15-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 07-Nov-14 | 07-Nov-14 | 23 |
| L17-8208 | Final Clean (Entire Floor) | 2 | 2 | 07-Nov-14 | 11-Nov-14 | 21 |
| L15-8212 | Resolve Final Punchlist | 5 | 5 | 11-Nov-14 | 17-Nov-14 | 23 |
| L03-8214 | Floor Complete | 0 | 0 | | 11-Nov-14 | 27 |
| L14-8214 | Floor Complete | 0 | 0 | | 11-Nov-14 | 27 |
| L16-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 12-Nov-14 | 12-Nov-14 | 21 |
| L16-8212 | Resolve Final Punchlist | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 21 |
| L17-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 17-Nov-14 | 17-Nov-14 | 18 |
| L15-8214 | Floor Complete | 0 | 0 | | 17-Nov-14 | 23 |
| L17-8212 | Resolve Final Punchlist | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 18 |
| L16-8214 | Floor Complete | 0 | 0 | | 19-Nov-14 | 21 |
| L17-8214 | Floor Complete | 0 | 0 | | 24-Nov-14 | 18 |
| **Mech Penthouse** | | | | | | |
| PH-8102 | PH - Complete GWB Hang / Tape / Finish | 7 | 7 | 18-Sep-14 | 26-Sep-14 | 8 |
| PH-8100 | PH - Insulation | 3 | 3 | 18-Sep-14 | 22-Sep-14 | 8 |
| PH-8104 | PH - Int Painting | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 8 |
| PH-8122 | PH - Plumbing Trim / Finish | 10 | 10 | 03-Oct-14 | 16-Oct-14 | 8 |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 26 |
| PH-8114 | PH - Signage | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 42 |

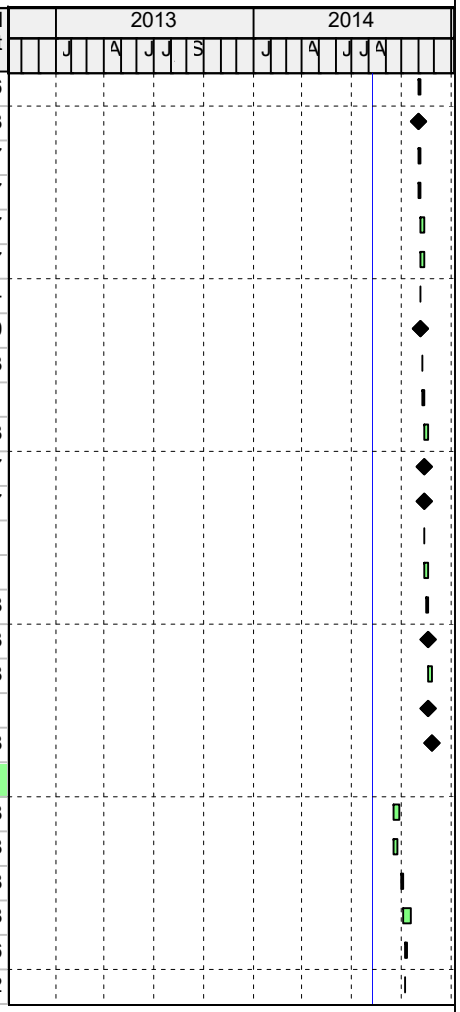



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-8108 | PH - Elec Trim / Finish | 10 | 10 | 17-Oct-14 | 30-Oct-14 | 8 |
| PH-8110 | PH - HVAC Trim / Finish | 10 | 10 | 17-Oct-14 | 30-Oct-14 | 12 |
| PH-8118 | PH - Elec Specialties Trim / Finish | 4 | 4 | 31-Oct-14 | 05-Nov-14 | 8 |
| PH-8124 | PH - Flooring | 4 | 4 | 06-Nov-14 | 12-Nov-14 | 8 |
| PH-8126 | PH - Doors & Hardware | 3 | 3 | 11-Nov-14 | 13-Nov-14 | 8 |
| PH-8134 | PH - Pre-Clean | 3 | 3 | 14-Nov-14 | 18-Nov-14 | 8 |
| PH-8132 | PH - Contractor Pre-Punchlist | 5 | 5 | 19-Nov-14 | 25-Nov-14 | 8 |
| PH-8208 | PH - Final Clean | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 8 |
| PH-8210 | PH - Owner Walk / Create Punchlist | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 8 |
| PH-8212 | PH - Final Punchlist | 5 | 5 | 04-Dec-14 | 10-Dec-14 | 8 |
| PH-8214 | PH - Floor Complete | 0 | 0 | | 10-Dec-14 | 8 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| **Smoke Control** | | | | | | |
| CO-7104 | Smoke Control Pre-Testing (Podium) | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 4 |
| CO-7106 | City of Bellevue Smoke Control Testing (Podium) | 5 | 5 | 10-Dec-14 | 16-Dec-14 | 4 |
| CO-7108 | Final Marriott Smoke Control Testing | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 4 |
| **Fire Sprinklers** | | | | | | |
| CO-7110 | Fire Sprinkler Pre-Testing (Podium) | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 4 |
| CO-7112 | City of Bellevue Fire Sprinkler Inspection / Approval (F | 5 | 5 | 10-Dec-14 | 16-Dec-14 | 4 |
| CO-7114 | Marriott Fire Sprinkler Testing | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 4 |
| **Fire Alarm** | | | | | | |
| CO-7116 | Fire Alarm Pre-Testing (Podium) | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 4 |
| CO-7118 | City of Bellevue Fire Alarm Inspection / Approval (Pod | 5 | 5 | 10-Dec-14 | 16-Dec-14 | 4 |
| CO-7120 | Marriott Fire Alarm Testing | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 4 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| CO-7100 | CO - Preliminary Start-Up & Testing (Podium) | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 21 |
| CO-7102 | CO - HVAC Commissioning (Podium) | 5 | 5 | 05-Nov-14 | 12-Nov-14 | 26 |

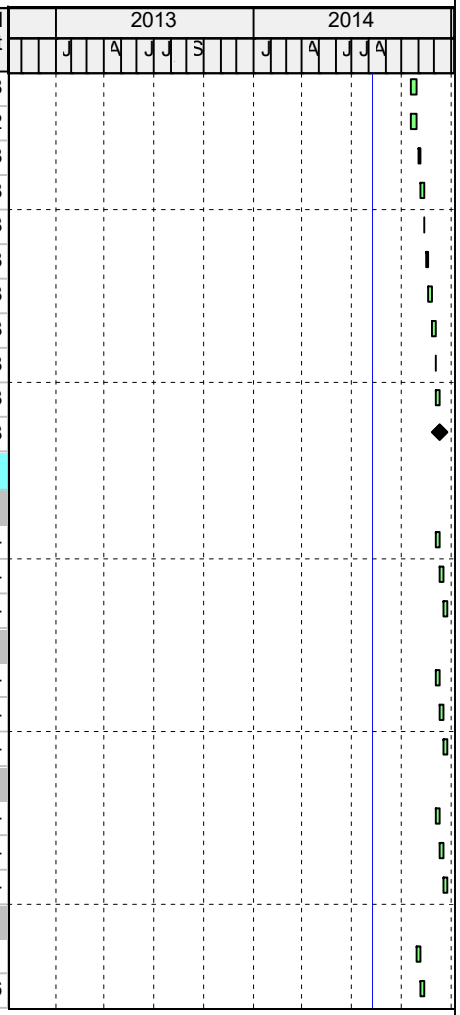


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Working Schedule - 9-7-14 Update** | | | | | | |
| I-1500 | Owner release revised LV design - Tower (ASIs 5, 13, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-1550 | Owner release revised LV design - Podium (ASIs 5, 1 | 200 | 0 | 23-May-13 A | 28-Apr-14 A | |
| I-1900 | Owner issue design revisions (ASIs 4, 9, 19, 34) | 215 | 0 | 23-May-13 A | 24-Mar-14 A | |
| I-2500 | Owner issue LL1 electrical revisions (ASIs 7, 9r2, 14, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-3400 | Owner provide Level 2 ceiling heights | 180 | 0 | 24-Jun-13 A | 24-Mar-14 A | |
| I-3700 | Owner resolve wall condition between stair and Eleva | 200 | 0 | 27-Jun-13 A | 16-Jun-14 A | |
| MM-1000 | MM - Temporary Power Available | 0 | 0 | 08-Jul-13 A | | |
| I-2100 | Owner revise roof steel design (Submittals 365, 370, | 200 | 0 | 09-Jul-13 A | 07-Apr-14 A | |
| I-2200 | Owner resolve elevator steel issue (RFI 112, RFI 112. | 200 | 0 | 09-Jul-13 A | 03-Mar-14 A | |
| I-2400 | Owner provide Tower light fixture selections (ASI 36) | 185 | 0 | 18-Jul-13 A | 08-Apr-14 A | |
| I-2900 | Owner revise Food Service and Kitchen (ASIs 11, 12, | 140 | 0 | 08-Aug-13 A | 27-Feb-14 A | |
| I-1400 | Owner develop envelope redesign | 70 | 0 | 27-Aug-13 A | 12-Dec-13 A | |
| I-3600 | Owner closeout glass/glazing allowance | 160 | 0 | 04-Sep-13 A | 30-Apr-14 A | |
| I-1200 | Owner release revised Concierge Lounge design (AS | 160 | 0 | 06-Sep-13 A | 08-Apr-14 A | |
| I-2800 | Owner revise interior public space design (ASIs 16, 1 | 130 | 0 | 25-Sep-13 A | 09-Apr-14 A | |
| I-2000 | Owner approve door frames (Submittals 258, 454, 48 | 85 | 0 | 27-Sep-13 A | 23-Jan-14 A | |
| I-3100 | Owner revise ballroom ceiling design (ASIs 18, 25) | 100 | 0 | 17-Oct-13 A | 25-Feb-14 A | |
| I-1600 | Owner provide directive for south & east corridor encl | 110 | 0 | 28-Oct-13 A | 18-Apr-14 A | |
| I-2300 | Owner resolve fire smoke dampers issue (RFI 233) | 115 | 0 | 30-Oct-13 A | 11-Apr-14 A | |
| I-2600 | Owner resolve L2 slab coordination issue | 4 | 0 | 13-Nov-13 A | 16-Nov-13 A | |
| I-2700 | Owner revise tower guest rooms design (ASIs 23, 29) | 58 | 0 | 04-Dec-13 A | 26-Feb-14 A | |
| I-1700 | Owner provide design for dry site utilities (ASIs 20, 20 | 66 | 0 | 09-Dec-13 A | 13-Mar-14 A | |
| I-1402 | Begin exterior panel production | 41 | 0 | 13-Dec-13 A | 12-Feb-14 A | |
| I-1300 | Owner issue "Hold" directive (email) | 0 | 0 | | 19-Dec-13 A | |
| I-1100 | Owner release revised L17 design (ASI 23, 29R1) | 74 | 0 | 20-Dec-13 A | 08-Apr-14 A | |
| I-1302 | Owner issue ASI 30 (Prep Kitchen Revisions) | 47 | 0 | 20-Dec-13 A | 27-Feb-14 A | |

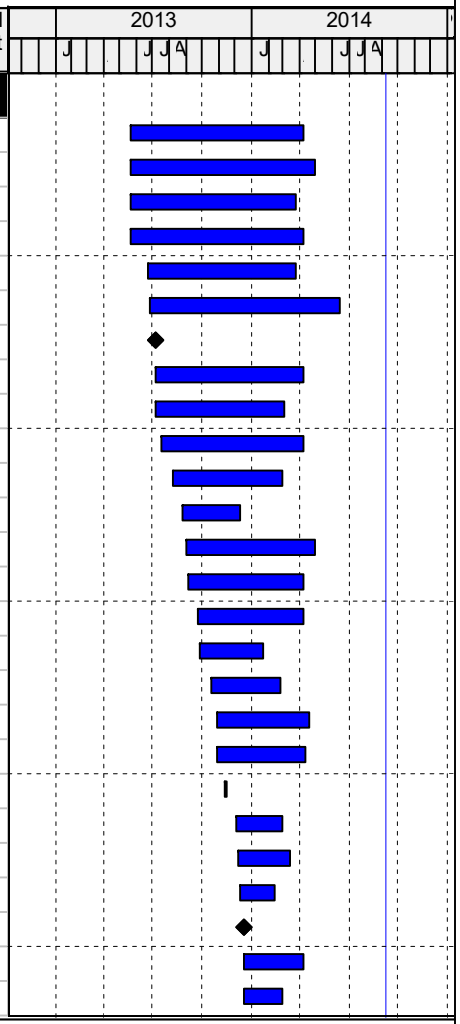


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| High Rise Hotel Sample Project | All Activities | Schedule Status Date 08-Sep-14 |
|---|---|---|

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1404 | City of Bellevue Approval | 90 | 0 | 23-Dec-13 A | 15-Jul-14 A | |
| I-3000 | Owner revise bar area (change to straight bar, IDRFI-( | 71 | 0 | 22-Jan-14 A | 27-May-14 A | |
| I-1306 | Prep Kitchen - Additional plumbing (ASI 30) | 4 | 0 | 17-Feb-14 A | 01-Aug-14 A | |
| I-2202 | Fabricate revised elevator steel | 60 | 0 | 04-Mar-14 A | 07-May-14 A | |
| I-2704 | Framing "Go Back" work for ASIs 23, 29 - L4 | 1 | 0 | 05-Mar-14 A | 12-Mar-14 A | |
| I-3900 | RFI 471, Resolve Ballroom parapet height issue | 1 | 0 | 08-Mar-14 A | 07-May-14 A | |
| I-1702 | Owner provide directive to proceed | 26 | 0 | 14-Mar-14 A | 01-May-14 A | |
| I-3300 | Owner provide Guest Room plumbing fixture selectio | 1 | 0 | 20-Mar-14 A | 20-Mar-14 A | |
| I-1902 | Procure revised structural steel | 15 | 0 | 25-Mar-14 A | 14-Apr-14 A | |
| I-4000 | Owner complete design of east stitched enclosure (fo | 1 | 0 | 01-Apr-14 A | 14-May-14 A | |
| I-2102 | Fabricate revised roof steel | 20 | 0 | 08-Apr-14 A | 15-May-14 A | |
| I-3200 | Owner provide light fixture selections for podium level | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| I-3800 | Resolve Heat Pump Electrical Overcurrent Issue | 20 | 0 | 23-Apr-14 A | 18-Jun-14 A | |
| L10-8221 | HVAC Risers Duct Insulation | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L11-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| I-2304 | Framing "Go Back" work at L3 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2306 | Framing "Go Back" work at L4 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2308 | Framing "Go Back" work at L5 for RFI 233 | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2706 | Framing "Go Back" work for ASIs 23, 29 - L5 | 1 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2708 | Framing "Go Back" work for ASIs 23, 29 - L6 | 1 | 0 | 29-Apr-14 A | 09-May-14 A | |
| I-2702 | Framing "Go Back" work for ASIs 23, 29 - L3 | 1 | 0 | 01-May-14 A | 01-May-14 A | |
| I-1706 | PSE scheduling delay | 10 | 0 | 01-May-14 A | 20-May-14 A | |
| I-3602 | Complete shop drawings & fab/deliver storefront fram | 40 | 0 | 01-May-14 A | 14-Jun-14 A | |
| L04-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| I-1802 | Rework framing for door hold-opens - LL4 | 1 | 0 | 07-May-14 A | 08-May-14 A | |
| L04-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-May-14 A | 12-May-14 A | |

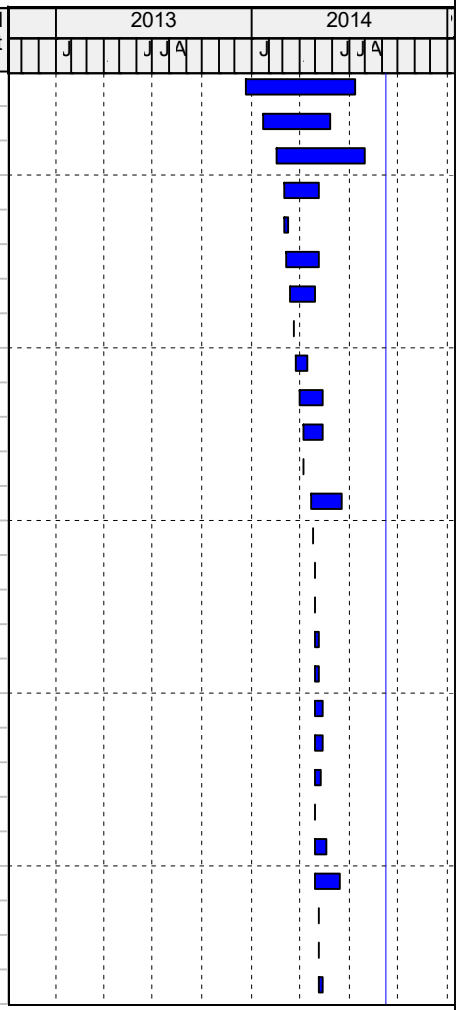



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1800 | Owner issue directive to proceed with door hold-open | 1 | 0 | 08-May-14 A | 08-May-14 A | |
| I-1804 | Rework framing for door hold-opens - LL3 | 1 | 0 | 08-May-14 A | 09-May-14 A | |
| I-2312 | Framing "Go Back" work at L7 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-2314 | Framing "Go Back" work at L8 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-3902 | Install Ballroom parapet extension | 5 | 0 | 08-May-14 A | 13-May-14 A | |
| I-1806 | Rework framing for door hold-opens - LL2 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-1808 | Rework framing for door hold-opens - LL1 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-2310 | Framing "Go Back" work at L6 for RFI 233 | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| I-2710 | Framing "Go Back" work for ASIs 23, 29 - L7 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| L05-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L06-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L05-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| LL2E-8110 | LL2 - Electrical, Fire pumps/equipment final connectic | 5 | 2 | 12-May-14 A | 29-Sep-14 | 37 |
| PH-8704 | PH - Install Machine Support Steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| PH-8710 | Install elevator rail support steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| L03-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L03-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 13-May-14 A | 14-May-14 A | |
| I-4002 | East Stitched - Install framing and windows | 9 | 0 | 19-May-14 A | 09-Jun-14 A | |
| L10-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L11-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L12-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| RF-4038 | AR - Concrete pads and curbs | 5 | 0 | 21-May-14 A | 04-Jun-14 A | |
| L10-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L11-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L12-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L14-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |

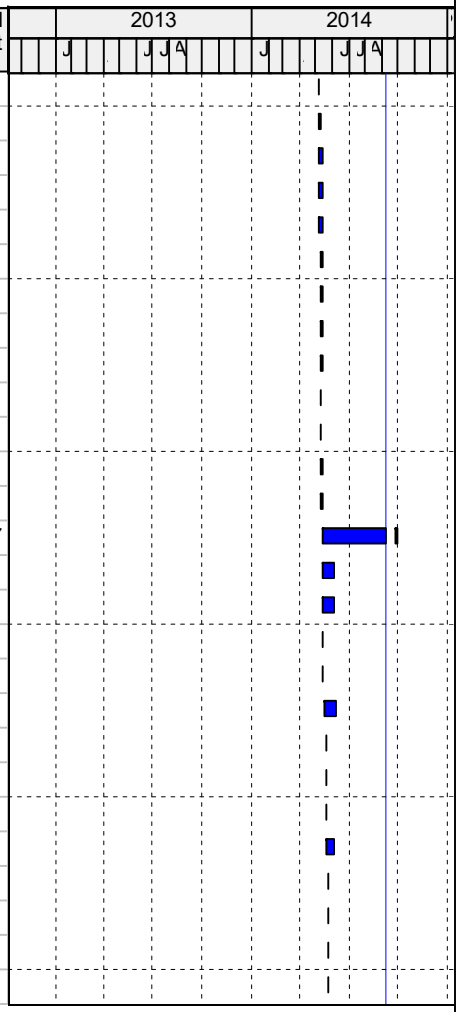



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 27-May-14 A | |
| L11-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 07-Jun-14 A | |
| L12-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 27-May-14 A | 06-Jun-14 A | |
| I-3002 | City of Bellevue approve bar design changes. | 5 | 2 | 28-May-14 A | 09-Sep-14 | 1 |
| L16-8221 | HVAC Risers Duct Insulation | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| PH-8712 | PH - Complete Framing and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| PH-8714 | Stage PH/L18 roofing materials | 2 | 0 | 30-May-14 A | 30-May-14 A | |
| L08-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L08-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 02-Jun-14 A | 20-Jun-14 A | |
| PH-8704I | Correct support steel embeds | 2 | 0 | 02-Jun-14 A | 11-Jun-14 A | |
| L14-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 03-Jun-14 A | 04-Jun-14 A | |
| L17-8221 | HVAC Risers Duct Insulation | 1 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| PC-4010 | PC - Fireproof Entry Roof Steel | 5 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| I-4100 | Owner resolve trap primers issue (RFI 560) | 5 | 0 | 03-Jun-14 A | 20-Jun-14 A | |
| RF-6028 | Tower Roof - Structural Steel | 5 | 0 | 04-Jun-14 A | 17-Jun-14 A | |
| L14-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L1B-6005 | Head of Wall Fire Caulk at CMU (including East Servi | 2 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L14-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L15-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L16-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |

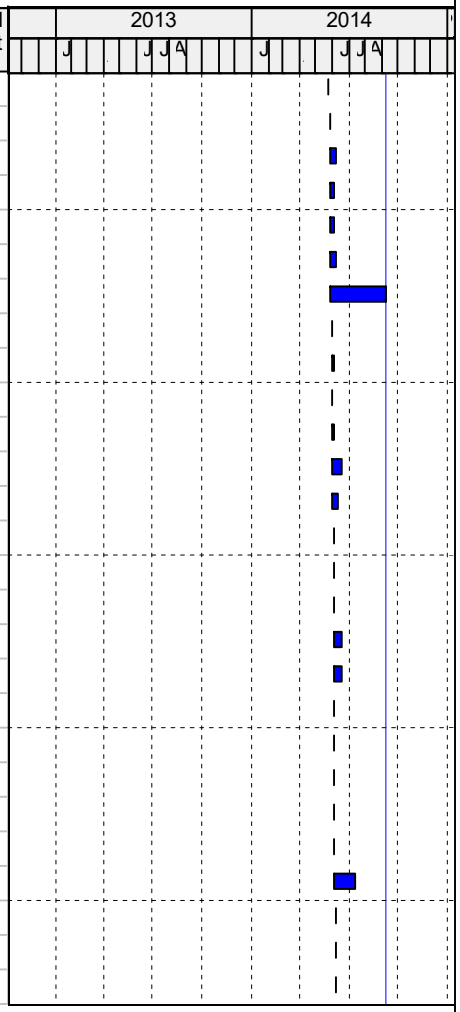



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 11-Jun-14 A | 12-Jun-14 A | |
| I-3702 | Complete wall framing at Stair/Elevator 5 (LL4) | 2 | 0 | 18-Jun-14 A | 20-Jun-14 A | |
| I-3720 | Fireproof added steel between Stair 1 and Elevator 5 | 5 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| I-3722 | Complete GWB between Stair 1 and Elevator 5 shaft | 10 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| LL1-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 22-Jul-14 A | |
| TC-5912 | Tower Crane pour-backs (LL4 to L3) | 4 | 0 | 19-Jun-14 A | 26-Jun-14 A | |
| LL1-Z2-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL4-6005 | LL4 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| LL3-6005 | LL3 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| L03-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 21-Jun-14 A | 21-Jun-14 A | |
| L06-6040 | Test Heat Pumps - L3, L4, L5 and L6 | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L03-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| L17-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL2-6005 | LL2 - Seismic Head Of Wall Fire Caulk at CMU | 5 | 0 | 24-Jun-14 A | 18-Jul-14 A | |
| I-3704 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL1-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z2-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z3-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 04-Aug-14 A | |
| L1L-6005 | Head of Wall Fire Caulk at CMU (including back of ho | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1K-6005 | Head of Wall Fire Caulk at CMU & Inspection | 2 | 0 | 24-Jun-14 A | 08-Aug-14 A | |
| L03-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L04-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| I-3710 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| I-3712 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| L1K-6018a | Install Kitchen hoods and grease ducts (OFCI) | 10 | 2 | 25-Jun-14 A | 09-Sep-14 | 22 |
| L03-8604 | L3 Pool - Plumbing R/I | 5 | 3 | 25-Jun-14 A | 23-Oct-14 | 12 |

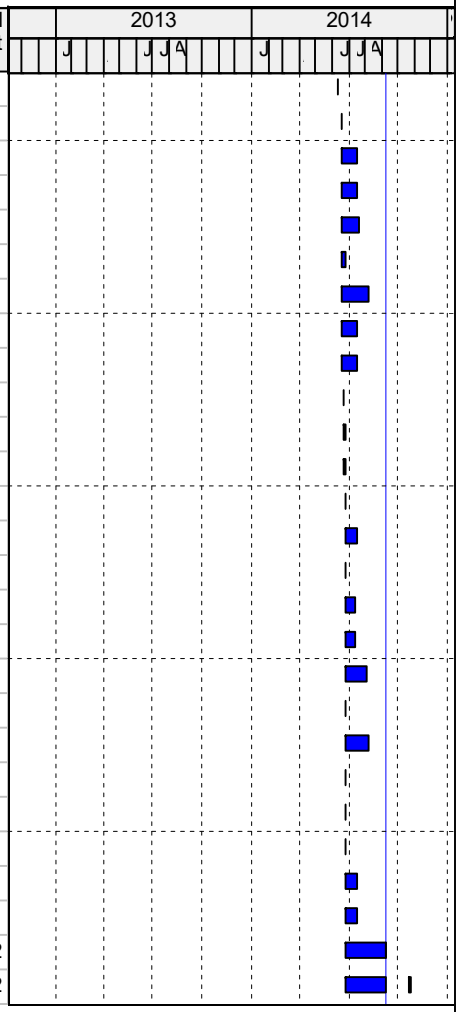



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 26-Jun-14 A | 03-Jul-14 A | |
| L09-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 26-Jun-14 A | 26-Jun-14 A | |
| I-3706 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 26-Jun-14 A | 10-Jul-14 A | |
| L03-8600 | L3 Pool - Framing & HM frames | 5 | 2 | 26-Jun-14 A | 20-Oct-14 | 12 |
| L05-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L08-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L04-7018 | Electrical Rough-In | 1 | 0 | 27-Jun-14 A | 22-Jul-14 A | |
| L04-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 27-Jun-14 A | 23-Jul-14 A | |
| L03-7020 | HVAC Rough-In | 1 | 0 | 29-Jun-14 A | 15-Jul-14 A | |
| L1RR-8100 | Insulation [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8100 | Insulation [DELETED - included in Ballroom activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8100 | Insulation [DELETED - included in Meeting Rooms ac | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8102 | GWB Hang [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8215 | GWB Tape [DELETED - included in Meeting Rooms a | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8104 | Prime Paint [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8102 | GWB Hang [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8215 | GWB Tape [DELETED - included in Ballroom activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8104 | Prime Paint [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8102 | GWB Hang [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |

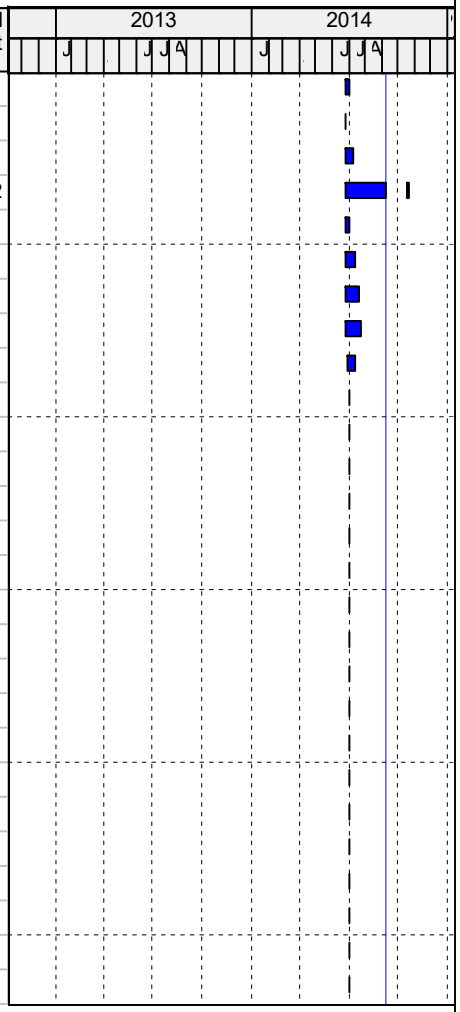


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1RR-8215 | GWB Tape [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8104 | Prime Paint [DELETED - included in Kitchen activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L03-7018 | Electrical Rough-In | 1 | 0 | 01-Jul-14 A | 14-Jul-14 A | |
| L03-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Jul-14 A | 15-Jul-14 A | |
| L10-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7102 | Install Vertical Heat Pump | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L03-7116 | Frame Walls | 1 | 0 | 02-Jul-14 A | 14-Jul-14 A | |
| L03-7118 | Install HM Door Frame | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L04-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L05-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L07-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L08-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L09-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L10-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L12-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| I-3708 | Complete wall framing at Stair/Elevator 5 (LL3) | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |

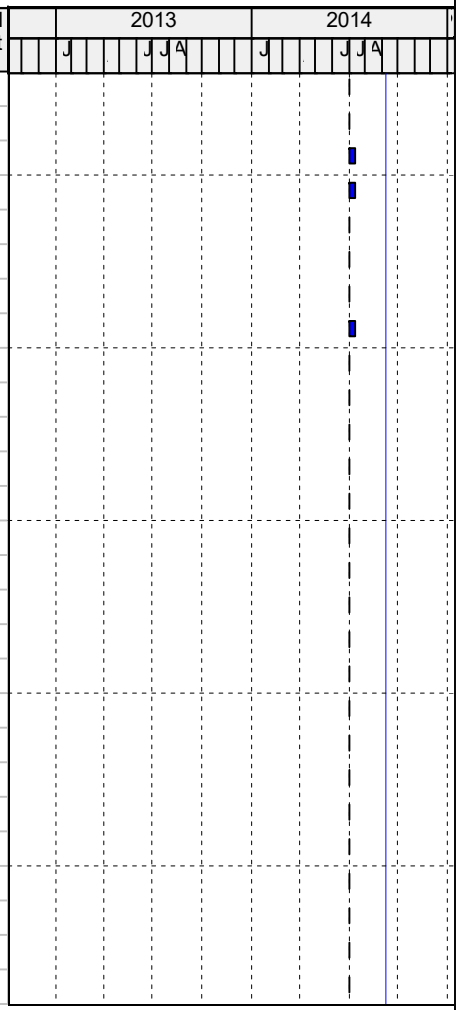



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 03-Jul-14 A | 07-Jul-14 A | |
| L04-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L05-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L06-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L07-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L08-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L17-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L10-6040 | Test Heat Pumps - L7, L8, L9 and L10 | 3 | 0 | 07-Jul-14 A | 09-Jul-14 A | |
| L10-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L03-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L04-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L05-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L06-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L07-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L08-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L09-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L10-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L12-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L14-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |

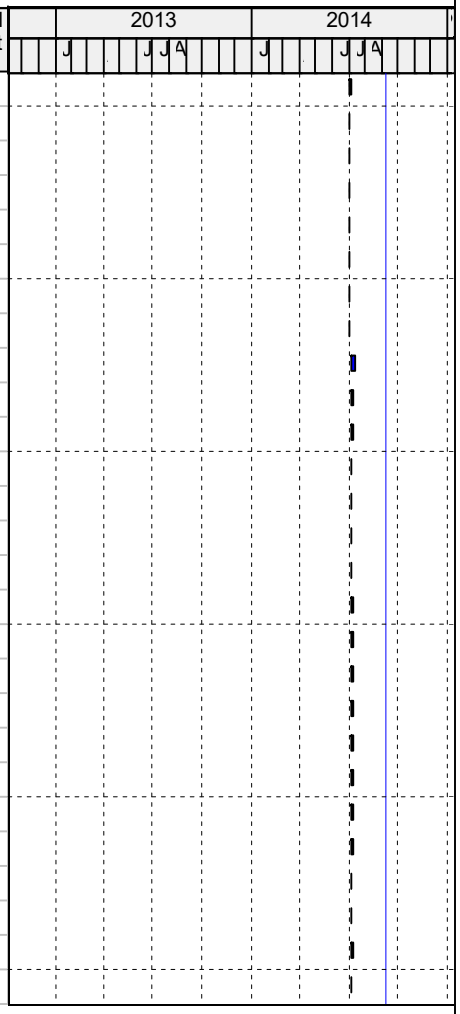



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Jul-14 A | 29-Jul-14 A | |
| L03-8602 | L3 Pool - Fire Sprinkler R/I | 5 | 0 | 08-Jul-14 A | 22-Jul-14 A | |
| L03-7016 | Install HM door frame | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L11-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L16-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 09-Jul-14 A | |
| L04-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |

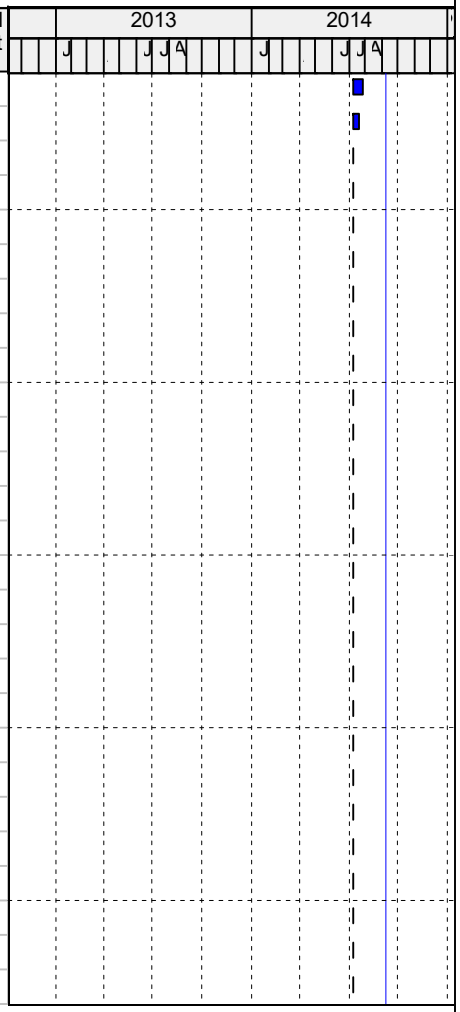



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L12-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| MP-FAB1 | Fabricate and Deliver Bronze Gold Horizontal Panels | 30 | 0 | 09-Jul-14 A | 15-Jul-14 A | |
| L04-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L05-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L06-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L16-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| MP-FAB2 | Fabricate and Deliver Silver Vertical Panels | 45 | 0 | 10-Jul-14 A | 25-Aug-14 A | |
| I-3004 | Issue ASI 38 | 0 | 0 | 11-Jul-14 A | | |
| I-3006 | Release bar area for x-ray examination | 5 | 0 | 11-Jul-14 A | 03-Sep-14 A | |
| L07-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| LL2-2046 | LL2 - Generator Room build-out | 20 | 15 | 14-Jul-14 A | 26-Sep-14 | 47 |
| LL1-Z2-6018a | Complete Mech RI at tower crane opening (LL1) | 4 | 0 | 14-Jul-14 A | 17-Jul-14 A | |
| L08-6223 | Frame Corridor Ceilings | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| SW-2006a | Complete Dry Utilities (Phase 2) | 5 | 0 | 14-Jul-14 A | 24-Jul-14 A | |
| L04-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L04-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L05-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L06-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |

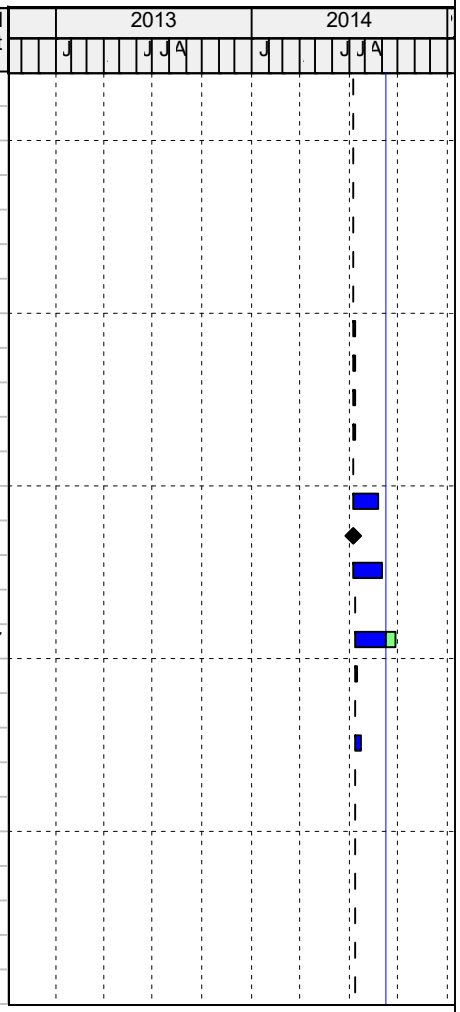



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L04-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L11-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L11-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L12-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L12-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L15-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L15-7102 | Install Vertical Heat Pump | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L1B-6026 | Install operable partition steel | 2 | 0 | 15-Jul-14 A | 08-Aug-14 A | |
| L09-6223 | Frame corridor ceilings | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L03-7120 | Electrical Rough-In | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |

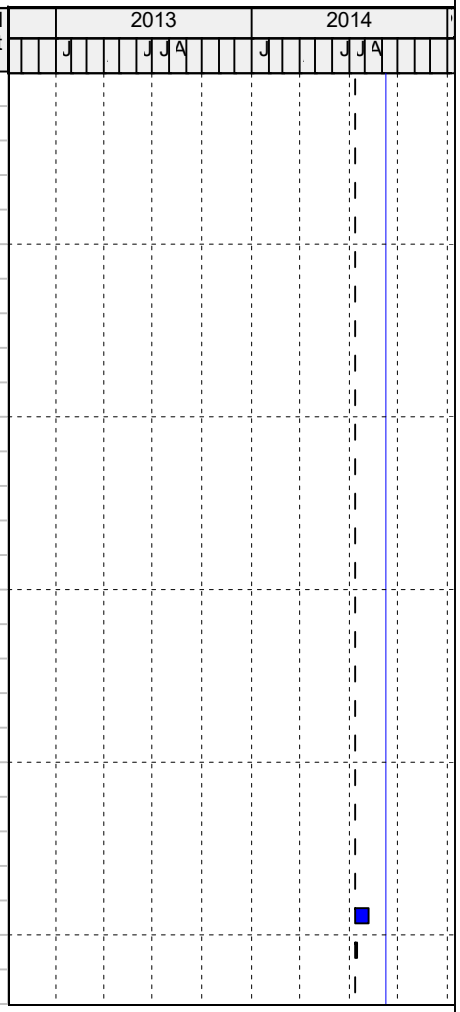



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L07-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L08-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L08-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L09-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L09-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L03-7142 | Install Laundry Chute (All Levels) | 9 | 0 | 15-Jul-14 A | 25-Jul-14 A | |
| LL2-2045 | LL2 - Electrical Room build-out | 15 | 5 | 15-Jul-14 A | 12-Sep-14 | 42 |
| L03-7122 | HVAC Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L04-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L05-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L06-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L07-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L07-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L08-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L08-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L09-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L09-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |

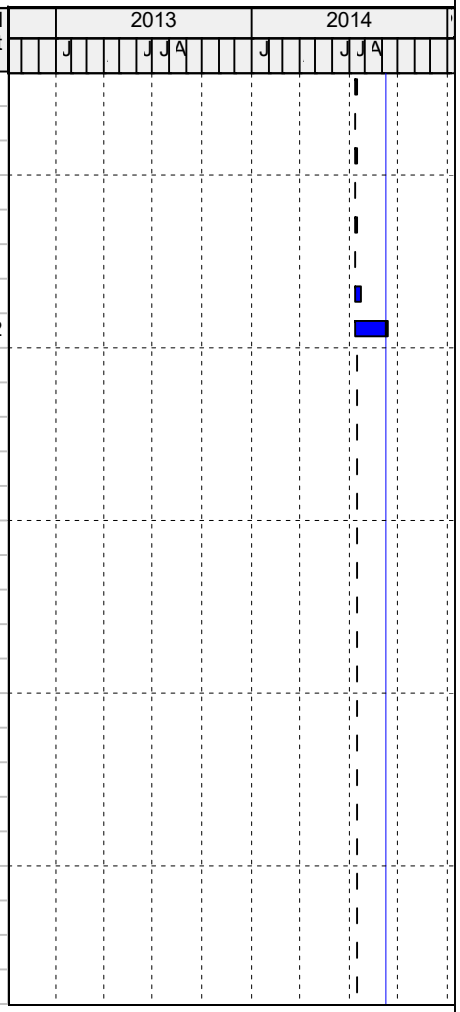



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L11-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L11-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L12-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L12-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L15-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L15-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L16-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L17-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L04-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L04-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L05-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L05-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L06-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L06-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L07-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L08-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L09-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |

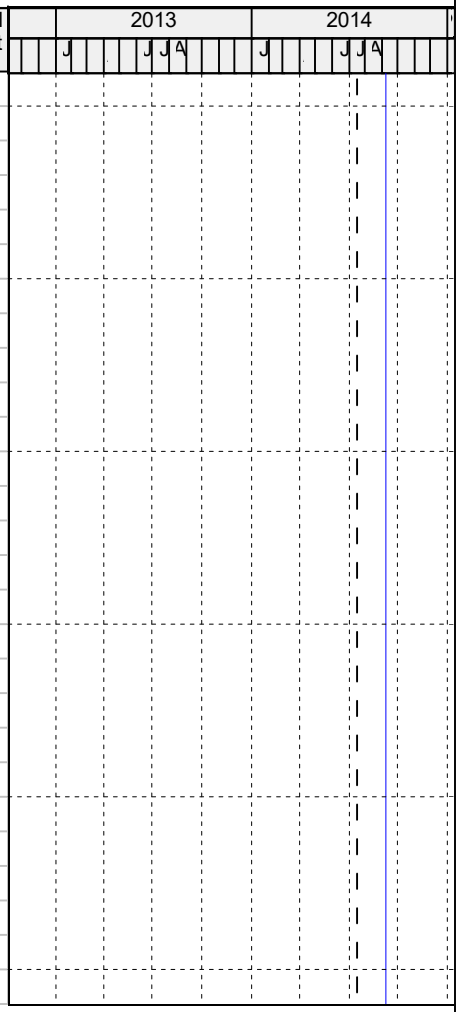



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L11-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L11-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L12-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L12-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L16-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L03-8608 | L3 Pool - Electrical R/I | 5 | 2 | 18-Jul-14 A | 22-Oct-14 | 13 |
| L03-8610 | L3 Pool - Fire Alarm / Elec Specialties R/I | 5 | 3 | 18-Jul-14 A | 23-Oct-14 | 12 |
| L15-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L15-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| L17-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L17-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| LL2-2052 | LL2 - Install fuel piping and exhaust duct to Generatc | 8 | 0 | 21-Jul-14 A | 15-Aug-14 A | |
| L04-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L04-7016 | Install HM door frame | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L07-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L08-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L10-7116 | Frame Walls | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L16-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 21-Jul-14 A | 22-Jul-14 A | |
| L16-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |

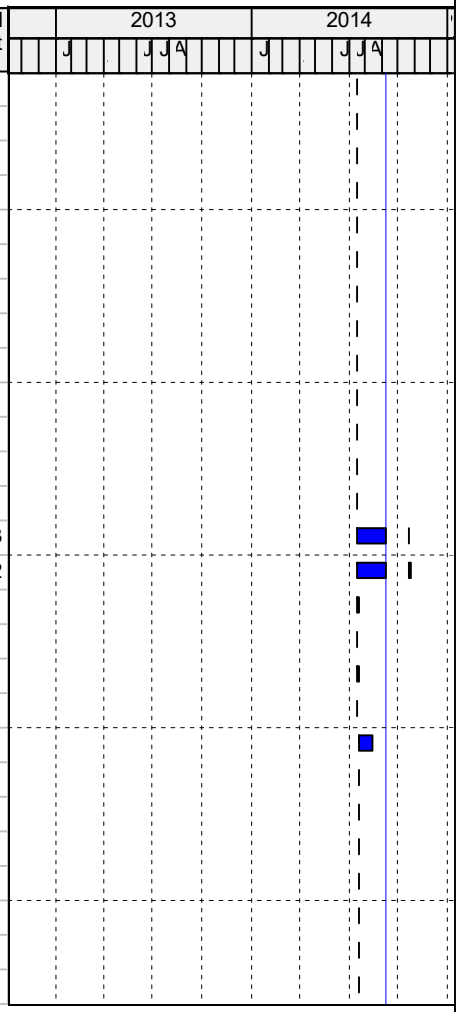



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| MPT-1002 | Tower - Install Elevation 35 (east elevation-south half) | 8 | 0 | 25-Jul-14 A | 04-Aug-14 A | |
| L16-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 25-Jul-14 A | 25-Jul-14 A | |
| L11-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L14-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L15-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L16-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L10-6223 | Frame Corridor Ceilings | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L11-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L15-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L15-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L11-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L14-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L16-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| I-1304 | Prep Kitchen - Additional framing (ASI 30) | 2 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-2302 | Framing "Go Back" work at LL1 for RFI 233 | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| I-2502 | Electrical rework at LL1 for ASIs 7, 9r2, 14, 27 | 4 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| L12-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L1B-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 01-Aug-14 A | 15-Aug-14 A | |
| MPL4-1000 | Upper L4 Ballroom - Install Elevations 1, 2 & 3 (south | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1000 | Tower - Install Elevations 26-27 (west elevation) [DEL | 13 | 0 | 01-Aug-14 A | 01-Aug-14 A | |

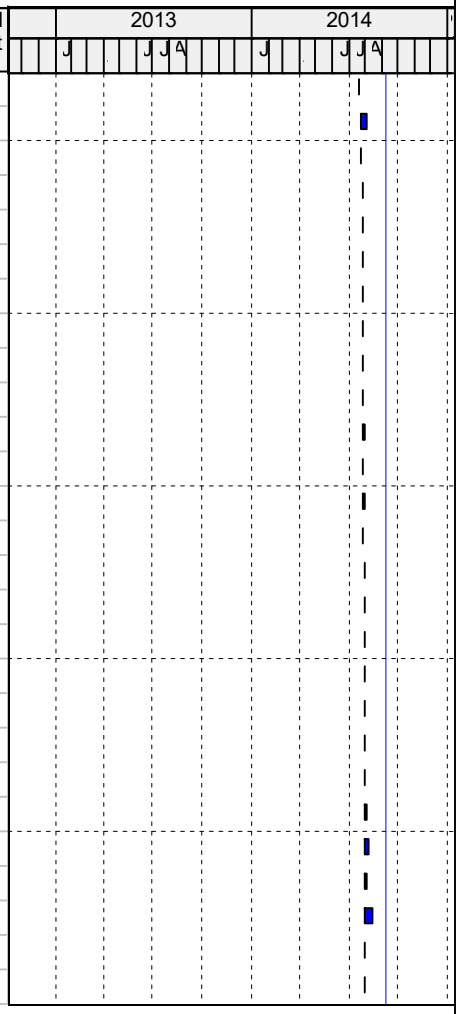



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPP-1002 | Podium - Install Elevations 1 & 2 (west elevation, sou | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPP-1008 | Podium - Install Elevations 7 & 8 (north & east elevati | 9 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1002 | Upper L4 Ballroom - Install Elevation 10 (west elevatic | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1004 | Upper L4 Ballroom - Install Elevation 9 (north elevatio | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1006 | Tower - Install Elevation 40 (east return-east end) [DE | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1010 | Tower - Install Elevations 51 (north elevation) [DELET | 8 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-4004 | East Stitched - Install metal panels [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L11-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L11-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L15-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L14-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L17-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| MPT-1010b | Tower - Install Elevation 45 [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L16-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 04-Aug-14 A | 05-Aug-14 A | |
| L11-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Aug-14 A | 08-Aug-14 A | |
| L04-7020 | HVAC Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |

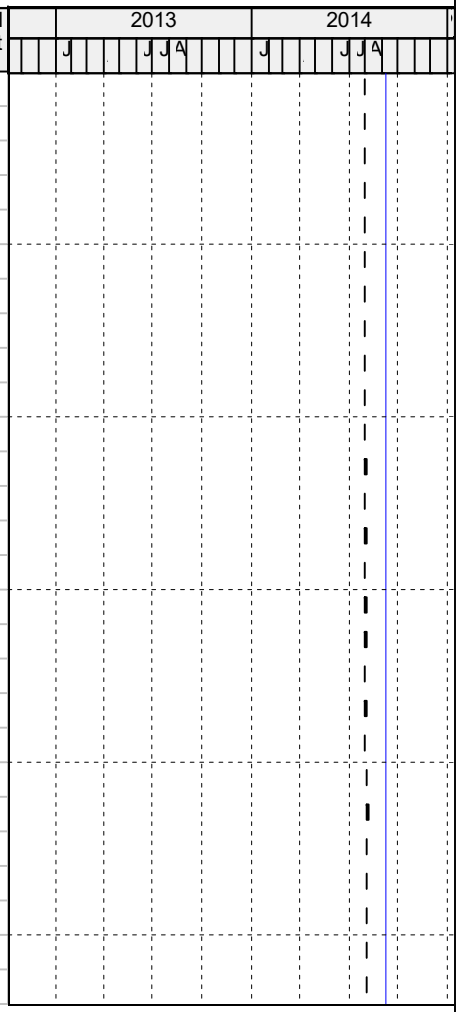



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L14-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L15-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 05-Aug-14 A | 07-Aug-14 A | |
| L05-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L06-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L07-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L08-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L09-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L10-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7018 | Electrical Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L14-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 05-Aug-14 A | 06-Aug-14 A | |
| L14-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| I-4104 | Install added trap primers - LL1 | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L06-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L07-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L08-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L09-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |

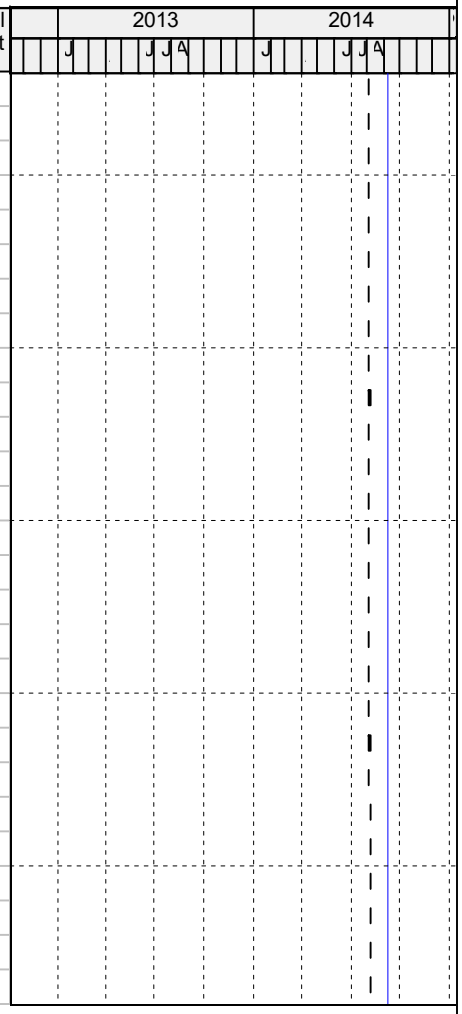



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7020 | HVAC Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L16-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| EL-1220 | Elevator fronts delivered | 0 | 0 | 07-Aug-14 A | | |
| L12-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L12-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-6223 | Frame Corridor Ceilings | 4 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L11-7016 | Install HM door frame | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L12-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L15-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L15-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L16-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L16-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L17-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L17-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-6040 | Test Heat Pumps - L11, L12 and L14 | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| PH-6026 | PH - Insulation/Vapor Barrier/GWB at Exterior Walls | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |

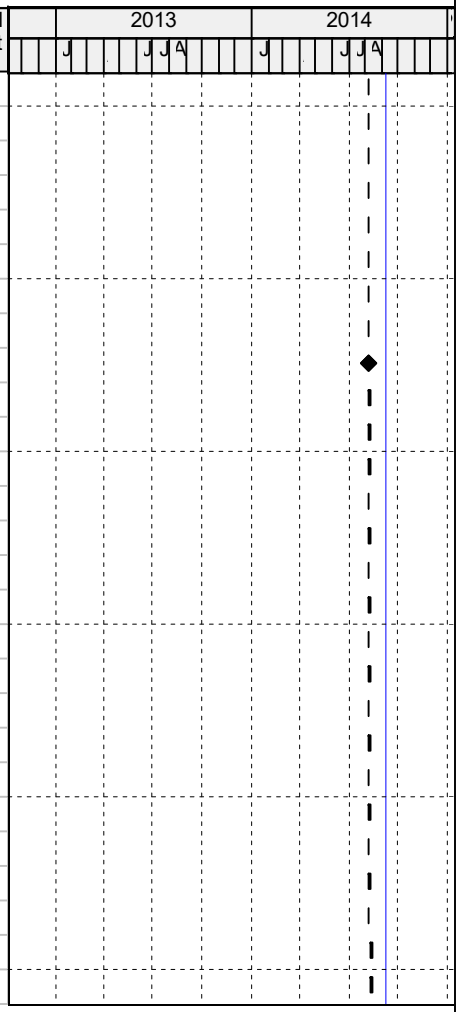



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L11-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-7026 | Inspections for GWB Cover | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 13-Aug-14 A | 13-Aug-14 A | |
| L15-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 14-Aug-14 A | 15-Aug-14 A | |
| LL2E-8108 | LL2 - Set fire pumps and equipment | 5 | 5 | 14-Aug-14 A | 25-Sep-14 | 37 |
| L10-7028 | GWB Hang/Tape/Finish | 5 | 4 | 14-Aug-14 A | 11-Sep-14 | 44 |
| L12-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L12-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L16-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L1BOH2-6008 | Int Wall Framing & Inspection | 5 | 0 | 14-Aug-14 A | 20-Aug-14 A | |
| I-4106 | Install added trap primers - L1 | 1 | 0 | 15-Aug-14 A | 15-Aug-14 A | |
| L14-6223 | Frame Corridor Ceilings | 4 | 0 | 15-Aug-14 A | 16-Aug-14 A | |
| L03-8136 | Install Counter Subtops | 3 | 0 | 15-Aug-14 A | 18-Aug-14 A | |
| LL2-2054 | LL2 - GWB, Hang 1st Layer at Laundry Room | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| LL2E-8112 | LL2 - Form/Pour Fire Pump Pads/Curbs | 2 | 0 | 16-Aug-14 A | 18-Aug-14 A | |
| LL1-6014Ia | L1 bar redesign - rework plumbing at ceilings | 10 | 5 | 18-Aug-14 A | 19-Sep-14 | 17 |

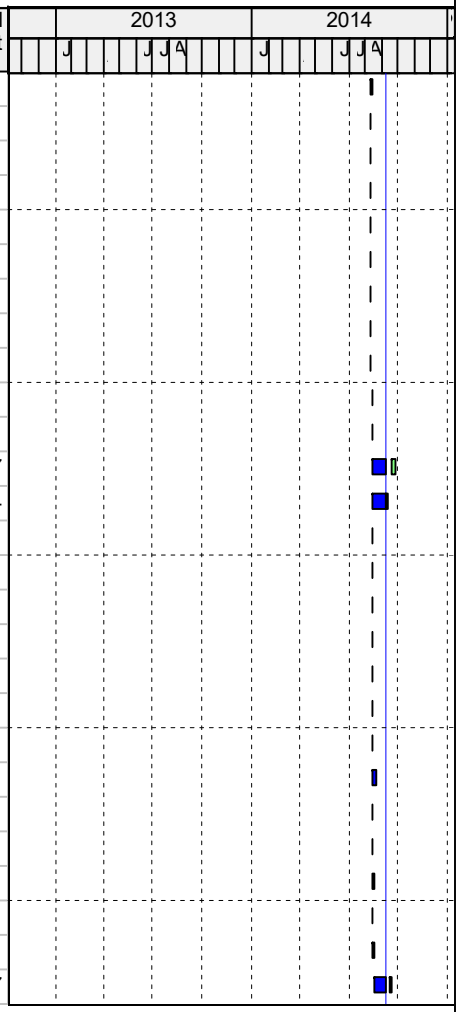



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6223 | Frame Corridor Ceilings | 4 | 0 | 18-Aug-14 A | 21-Aug-14 A | |
| L17-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Aug-14 A | 18-Aug-14 A | |
| L04-8136 | Install Counter Subtops | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-6014Ic | L1 bar redesign - rework electrical at ceilings | 10 | 5 | 18-Aug-14 A | 12-Sep-14 | 27 |
| LL2E-8114 | LL2 - Set Tube Steel at Door | 1 | 0 | 19-Aug-14 A | 19-Aug-14 A | |
| L17-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 20-Aug-14 A | 21-Aug-14 A | |
| L17-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 20-Aug-14 A | 20-Aug-14 A | |
| L05-8136 | Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 26-Aug-14 A | |
| L06-8136 | Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 25-Aug-14 A | |
| L16-6223 | Frame Corridor Ceilings | 4 | 0 | 21-Aug-14 A | 29-Aug-14 A | |
| L17-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 21-Aug-14 A | 22-Aug-14 A | |
| L17-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 21-Aug-14 A | 21-Aug-14 A | |
| L1BOH2-6016 | Electrical RI | 4 | 3 | 21-Aug-14 A | 10-Sep-14 | 22 |
| L1BOH2-6022 | Fire Alarm / Elec Specialties RI | 4 | 3 | 21-Aug-14 A | 10-Sep-14 | 22 |
| L1BOH2-6018 | HVAC RI | 4 | 3 | 21-Aug-14 A | 10-Sep-14 | 22 |
| L15-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7020 | HVAC Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7022 | Fire Sprinkler Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| LL2E-8116 | LL2 - Set Door Jamb | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L04-7028 | GWB Hang/Tape/Finish | 5 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L05-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L05-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L06-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |

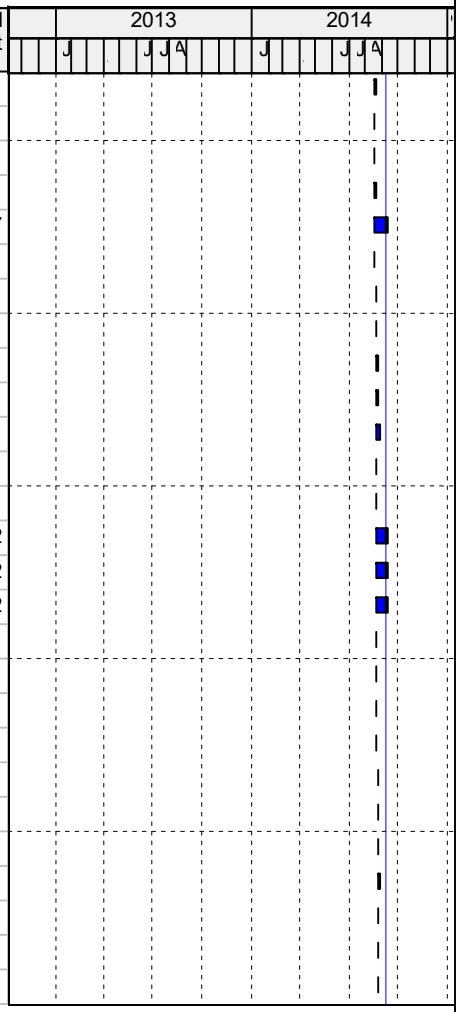



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L03-8123 | Bathroom "Barn Doors" On Site | 0 | 0 | 25-Aug-14 A | | |
| LL3-6026 | LL3 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL2-6026 | LL2 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL1-Z3-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L1BOH2-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |

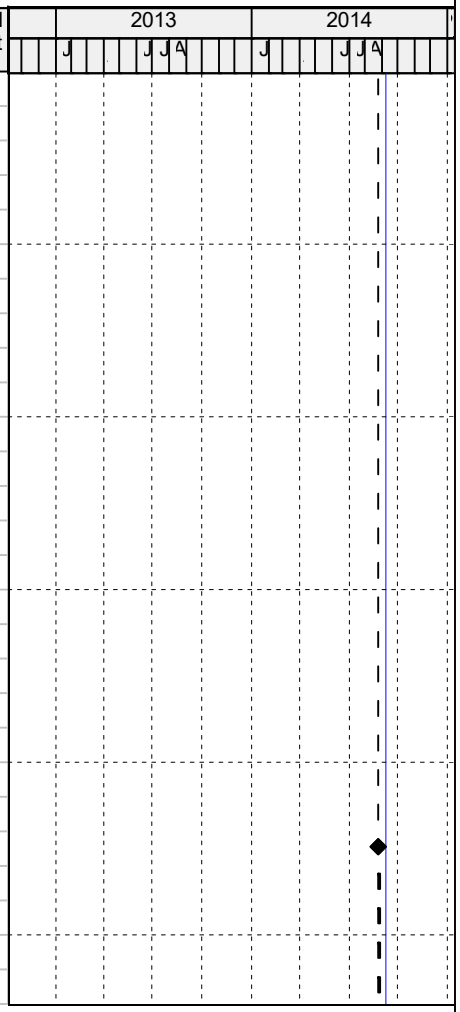



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-6026 | L2 - Set Elevator Fronts (Cars 1-4 | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L03-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L04-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L05-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L06-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L07-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L08-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L09-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L10-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L11-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L12-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L14-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L15-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L16-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L17-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| MPT-1008 | Tower - Install E/W Wing, N. Side West Half (Elev 50, | 7 | 1 | 26-Aug-14 A | 08-Sep-14 | 64 |
| L06-6005 | CMU Fire Caulk/Clips | 2 | 1 | 26-Aug-14 A | 08-Sep-14 | 29 |
| L07-6005 | CMU Fire Caulk/Clips | 2 | 1 | 26-Aug-14 A | 08-Sep-14 | 29 |
| L08-6005 | CMU Fire Caulk/Clips | 2 | 1 | 26-Aug-14 A | 08-Sep-14 | 29 |
| L05-7026 | Inspections for GWB Cover | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L05-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L11-7028 | GWB Hang/Tape/Finish | 5 | 3 | 26-Aug-14 A | 10-Sep-14 | 45 |
| L12-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L14-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L03-8105a | Painting - Split Door Jambs | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L09-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 08-Sep-14 | 29 |
| L10-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 08-Sep-14 | 29 |

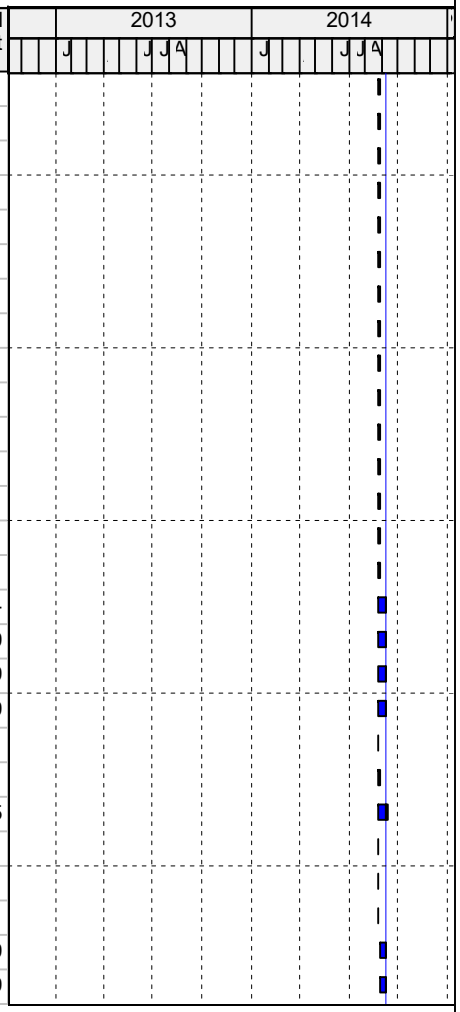



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 09-Sep-14 | 29 |
| L12-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 09-Sep-14 | 29 |
| L14-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 09-Sep-14 | 29 |
| L15-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 09-Sep-14 | 29 |
| L16-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 09-Sep-14 | 29 |
| L05-8201 | Install ACT Grid @ Corridors | 2 | 0 | 27-Aug-14 A | 28-Aug-14 A | |
| L16-7022 | Fire Sprinkler Rough-In | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L04-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L06-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| EP-5110a | L1 - Install Steel at Revolving Door Opening | 3 | 0 | 27-Aug-14 A | 29-Aug-14 A | |
| L05-8105a | Painting - Split Door Jambs | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L03-8124d | Flooring On Site and Acclimated | 2 | 0 | 29-Aug-14 A | 01-Sep-14 A | |
| L02-5102 | L2 - Storefront Frames | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| L04-6005 | CMU Fire Caulk/Clips | 2 | 1 | 02-Sep-14 A | 08-Sep-14 | 29 |
| L05-6005 | CMU Fire Caulk/Clips | 2 | 1 | 02-Sep-14 A | 08-Sep-14 | 29 |
| L17-6005 | CMU Fire Caulk/Clips | 2 | 1 | 02-Sep-14 A | 09-Sep-14 | 29 |
| L03-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L12-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L14-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| MPT-1014 | Tower - Install E/W Wing, N. Side, E. Half (Elev 46-49 | 8 | 6 | 02-Sep-14 A | 15-Sep-14 | 65 |
| L07-8136 | Install Counter Subtops | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| MPT-1004 | Tower - Install E/W Wing, S. Side w/o Windows (Elev | 6 | 5 | 03-Sep-14 A | 15-Sep-14 | 64 |
| L03-7028 | GWB Hang/Tape/Finish | 5 | 4 | 03-Sep-14 A | 11-Sep-14 | 44 |
| L12-7028 | GWB Hang/Tape/Finish | 5 | 4 | 03-Sep-14 A | 11-Sep-14 | 44 |
| L17-6223 | Frame Corridor Ceilings | 4 | 3 | 04-Sep-14 A | 15-Sep-14 | 10 |
| L02-5104b | L2 - Install Storefront Temporary Enclosures | 1 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| I-3008 | Coordinate and perform x-ray examination | 7 | 5 | 04-Sep-14 A | 12-Sep-14 | 17 |

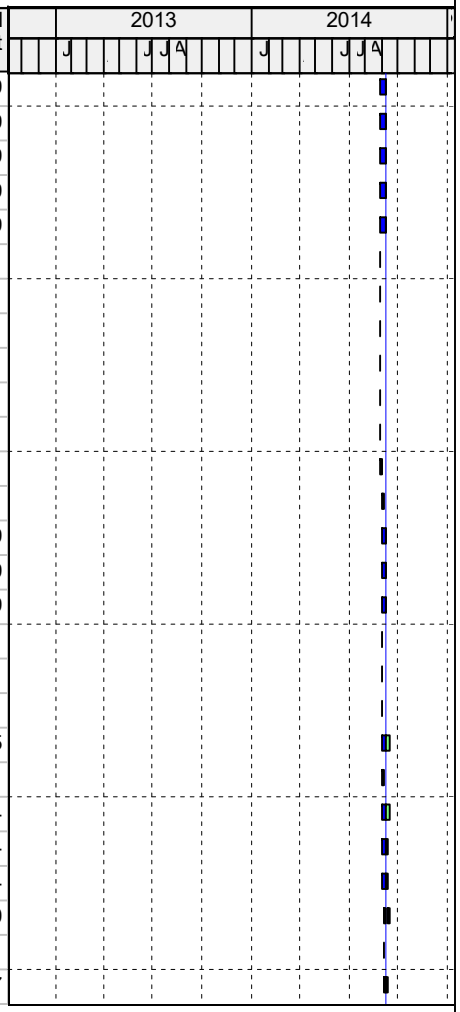



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-5104a | L2 - Measure/Fabricate Storefront Glazing | 15 | 14 | 05-Sep-14 A | 25-Sep-14 | 32 |
| L16-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 16 |
| L16-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 17 |
| L07-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 60 |
| LL2E-8340 | LL2 - Install walk-in cooler/freezer (BY OTHERS) | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 32 |
| L03-8395 | Framing at Elevator Lobby | 3 | 3 | 08-Sep-14 | 10-Sep-14 | 26 |
| L04-8395 | Framing at Elevator Lobby | 3 | 3 | 08-Sep-14 | 10-Sep-14 | 26 |
| L05-8395 | Framing at Elevator Lobby | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 26 |
| L06-8395 | Framing at Elevator Lobby | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 31 |
| RF-4008 | Tower Roof - Coping / Flashing | 10 | 10 | 08-Sep-14 | 19-Sep-14 | 67 |
| I-4102 | Install added trap primers - LL2 | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 40 |
| I-4108 | Install added trap primers - L2 | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 37 |
| I-4110 | Install added trap primers - L3 | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 16 |
| I-4112 | Install added trap primers - Roof PH | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 17 |
| L03-7128 | Inspections for GWB Cover | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 48 |
| L04-7030 | Paint | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 48 |
| L05-7030 | Paint | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 51 |
| L06-7026 | Inspections for GWB Cover | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 42 |
| L07-7026 | Inspections for GWB Cover | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 42 |
| L08-7026 | Inspections for GWB Cover | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 42 |
| L09-7026 | Inspections for GWB Cover | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 42 |
| L14-7028 | GWB Hang/Tape/Finish | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 43 |
| L15-7018 | Electrical Rough-In | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 40 |
| L16-7018 | Electrical Rough-In | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 41 |
| L17-7018 | Electrical Rough-In | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 40 |
| L04-7120 | Electrical Rough-In | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 46 |
| L05-7120 | Electrical Rough-In | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 46 |

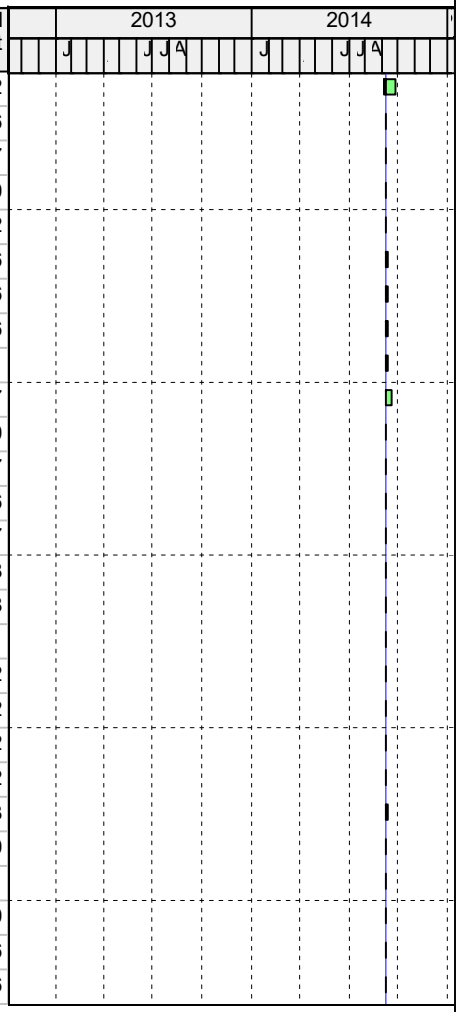



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7120 | Electrical Rough-In | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 46 |
| L07-7120 | Electrical Rough-In | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 46 |
| L08-7120 | Electrical Rough-In | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 46 |
| L09-7118 | Install HM Door Frame | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 47 |
| L09-7120 | Electrical Rough-In | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 45 |
| L10-7118 | Install HM Door Frame | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 47 |
| L10-7120 | Electrical Rough-In | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 45 |
| L11-7120 | Electrical Rough-In | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 45 |
| L12-7120 | Electrical Rough-In | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 45 |
| L14-7120 | Electrical Rough-In | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 45 |
| L15-7120 | Electrical Rough-In | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 45 |
| L16-7120 | Electrical Rough-In | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 46 |
| L17-7116 | Frame Walls | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 44 |
| L17-7118 | Install HM Door Frame | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 47 |
| EL-1228 | Construct/Approve elevator lobby framing mockup (L | 3 | 3 | 08-Sep-14 | 10-Sep-14 | 4 |
| L03-8138 | Install Toilet Accessories | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 10 |
| L03-8140 | Counterops On Site | 0 | 0 | 08-Sep-14* | | 36 |
| L03-8129a | Shower Doors On Site | 0 | 0 | 08-Sep-14* | | 50 |
| LL3-6028 | LL3 - Frame Elevator Lobby | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 30 |
| LL2-6032 | LL2 - Complete Framing (Including Elevator Lobby) | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 35 |
| LL1-Z3-6028 | Framing at Elevator Lobby | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 35 |
| L1BOH2-6028 | Framing at Elevator Lobby | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 17 |
| L02-6030 | L2 - Framing at Elevator Lobby | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 34 |
| L03-8200a | New murals on site (date estimated) | 0 | 0 | 08-Sep-14* | | 22 |
| L03-8200b | Install Guestroom Murals | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 22 |
| L1-5104b | L1 - Install Storefront Temporary Enclosures | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 4 |
| LL2E-8118 | LL2 - Frame Infill, Install Densglass & Inspect at Fire I | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 37 |

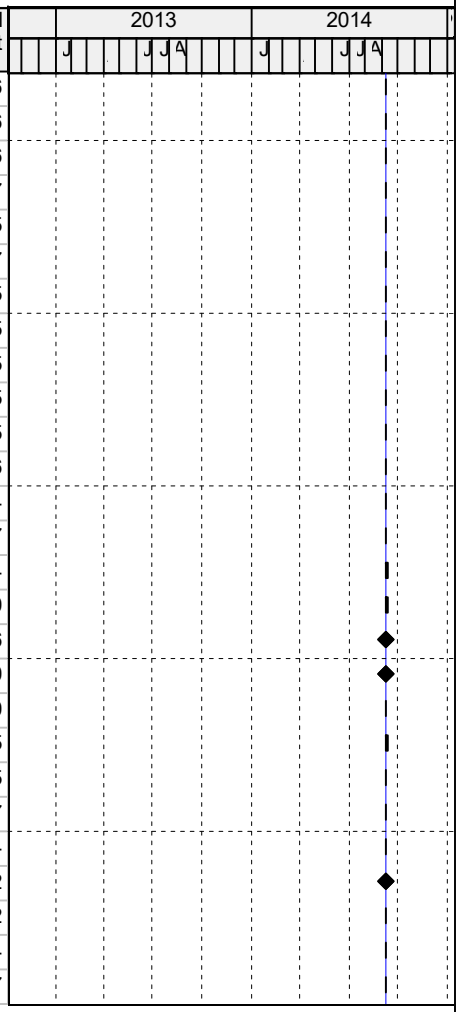



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-FCC10 | FCC - Set Jamb | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 38 |
| LL2-2058a | LL2 - GWB Hang 1st Layer | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 46 |
| LL2E-8342 | LL2 - Final connections at walk-in cooler/freezer | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 38 |
| L03-7130 | GWB Hang/Tape/Finish | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 48 |
| L04-7032 | Install VCT Flooring (x42) | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 48 |
| L05-7032 | Install VCT Flooring (x42) | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 51 |
| L06-7028 | GWB Hang/Tape/Finish | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 42 |
| L07-7028 | GWB Hang/Tape/Finish | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 42 |
| L08-7028 | GWB Hang/Tape/Finish | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 42 |
| L09-7028 | GWB Hang/Tape/Finish | 5 | 5 | 09-Sep-14 | 15-Sep-14 | 42 |
| L15-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 40 |
| L16-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 41 |
| L17-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 40 |
| L04-7122 | HVAC Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 46 |
| L04-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 46 |
| L05-7122 | HVAC Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 46 |
| L05-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 46 |
| L06-7122 | HVAC Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 46 |
| L06-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 46 |
| L07-7122 | HVAC Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 46 |
| L07-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 46 |
| L08-7122 | HVAC Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 46 |
| L08-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 46 |
| L09-7122 | HVAC Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 45 |
| L09-7124 | Fire Sprinkler Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 45 |
| L10-7122 | HVAC Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 45 |
| L10-7124 | Fire Sprinkler Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 45 |

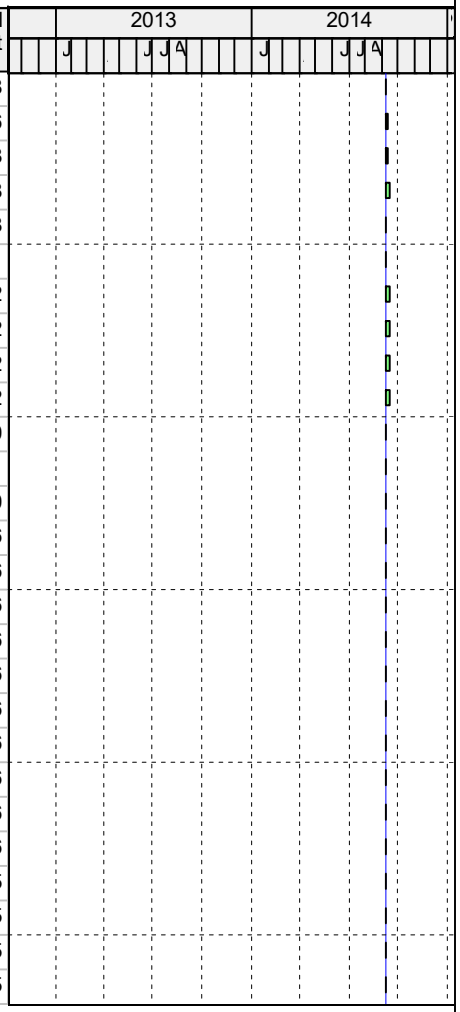



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7122 | HVAC Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 45 |
| L11-7124 | Fire Sprinkler Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 45 |
| L12-7122 | HVAC Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 45 |
| L12-7124 | Fire Sprinkler Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 45 |
| L14-7122 | HVAC Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 45 |
| L14-7124 | Fire Sprinkler Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 45 |
| L15-7122 | HVAC Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 45 |
| L15-7124 | Fire Sprinkler Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 45 |
| L16-7122 | HVAC Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 46 |
| L16-7124 | Fire Sprinkler Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 46 |
| L17-7120 | Electrical Rough-In | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 44 |
| L1BOH2-6030 | Electrical RI at Elevator Lobby | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 17 |
| LL1-Z3-FCC12 | FCC - Sheetrock Outside Wall | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 38 |
| MPT-1010a | Tower - Install E/W Wing, West End (Elev 52,53) | 8 | 8 | 09-Sep-14 | 18-Sep-14 | 68 |
| L03-8402 | Electrical Rough-In at Elevator Lobby | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 28 |
| L04-8402 | Electrical Rough-In at Elevator Lobby | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 27 |
| L03-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 28 |
| L04-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 27 |
| L07-8395 | Framing at Elevator Lobby | 4 | 4 | 10-Sep-14 | 13-Sep-14 | 31 |
| L08-8395 | Framing at Elevator Lobby | 4 | 4 | 10-Sep-14 | 13-Sep-14 | 31 |
| L04-7034 | Install Door and Hardware (x42) | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 48 |
| L05-7034 | Install Door and Hardware (x42) | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 51 |
| L15-7026 | Inspections for GWB Cover | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 40 |
| L16-7026 | Inspections for GWB Cover | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 41 |
| L17-7026 | Inspections for GWB Cover | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 40 |
| L04-7128 | Inspections for GWB Cover | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 46 |
| L05-7128 | Inspections for GWB Cover | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 46 |

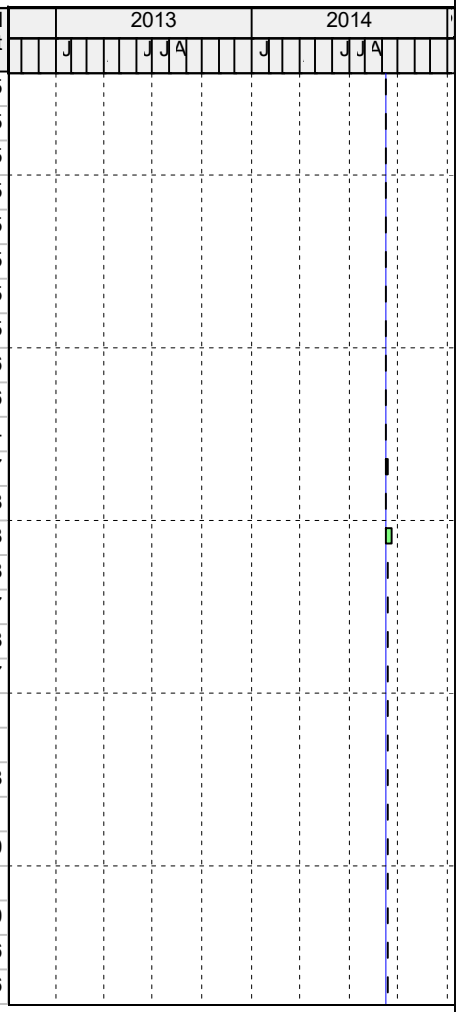



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7128 | Inspections for GWB Cover | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 46 |
| L07-7128 | Inspections for GWB Cover | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 46 |
| L08-7128 | Inspections for GWB Cover | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 46 |
| L09-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 45 |
| L10-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 45 |
| L11-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 45 |
| L12-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 45 |
| L14-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 45 |
| L15-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 45 |
| L16-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 46 |
| L17-7122 | HVAC Rough-In | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 44 |
| L17-7124 | Fire Sprinkler Rough-In | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 44 |
| L03-8126a | Doors & Hardware On Site | 0 | 0 | 10-Sep-14* | | 25 |
| LL3-6030 | LL3 - Electrical RI at Elevator Lobby | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 30 |
| LL1-Z3-6030 | Electrical RI at Elevator Lobby | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 35 |
| L02-6032 | L2 - Electrical RI at Elevator Lobby | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 34 |
| L04-8200a | Install Guestroom Murals | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 22 |
| LL2E-8120 | LL2 - Insulation, Vapor Barrier & Inspect at Fire Pump | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 37 |
| LL1-Z3-FCC14 | FCC - Verify Fire Caulk OK & Inspect Room OK to 2nd | 1 | 1 | 10-Sep-14 | 10-Sep-14 | 38 |
| L05-8402 | Electrical Rough-In at Elevator Lobby | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 28 |
| L06-8402 | Electrical Rough-In at Elevator Lobby | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 52 |
| L05-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 28 |
| L06-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 52 |
| L09-8395 | Framing at Elevator Lobby | 4 | 4 | 11-Sep-14 | 15-Sep-14 | 31 |
| L10-8395 | Framing at Elevator Lobby | 4 | 4 | 11-Sep-14 | 15-Sep-14 | 31 |
| L04-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 11-Sep-14 | 15-Sep-14 | 48 |
| L05-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 11-Sep-14 | 15-Sep-14 | 51 |

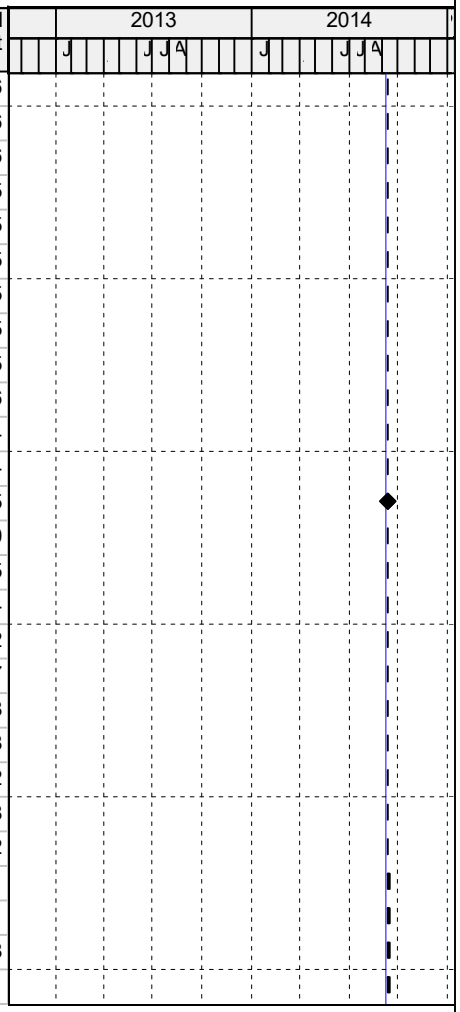



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7030 | Paint | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 45 |
| L15-7028 | GWB Hang/Tape/Finish | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 40 |
| L16-7028 | GWB Hang/Tape/Finish | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 41 |
| L17-7028 | GWB Hang/Tape/Finish | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 40 |
| L04-7130 | GWB Hang/Tape/Finish | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 46 |
| L05-7130 | GWB Hang/Tape/Finish | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 46 |
| L06-7130 | GWB Hang/Tape/Finish | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 46 |
| L07-7130 | GWB Hang/Tape/Finish | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 46 |
| L08-7130 | GWB Hang/Tape/Finish | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 46 |
| L09-7128 | Inspections for GWB Cover | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 45 |
| L10-7128 | Inspections for GWB Cover | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 45 |
| L11-7128 | Inspections for GWB Cover | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 45 |
| L12-7128 | Inspections for GWB Cover | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 45 |
| L14-7128 | Inspections for GWB Cover | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 45 |
| L15-7128 | Inspections for GWB Cover | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 45 |
| L16-7128 | Inspections for GWB Cover | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 46 |
| L17-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 44 |
| L1BOH2-8130 | Inspections For Cover | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 22 |
| LL1-Z3-FCC16 | FCC - GWB, Hang 2nd Layer | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 38 |
| L03-8405 | Cover Inspection | 1 | 1 | 12-Sep-14 | 12-Sep-14 | 28 |
| L04-8405 | Cover Inspection | 1 | 1 | 12-Sep-14 | 12-Sep-14 | 27 |
| L11-8395 | Framing at Elevator Lobby | 3 | 3 | 12-Sep-14 | 15-Sep-14 | 31 |
| L12-8395 | Framing at Elevator Lobby | 4 | 4 | 12-Sep-14 | 16-Sep-14 | 31 |
| L03-8129 | Install Shower Doors | 4 | 4 | 12-Sep-14 | 17-Sep-14 | 46 |
| L03-7030 | Paint | 1 | 1 | 12-Sep-14 | 12-Sep-14 | 44 |
| L10-7030 | Paint | 1 | 1 | 12-Sep-14 | 12-Sep-14 | 44 |
| L11-7032 | Install VCT Flooring (x42) | 1 | 1 | 12-Sep-14 | 12-Sep-14 | 45 |

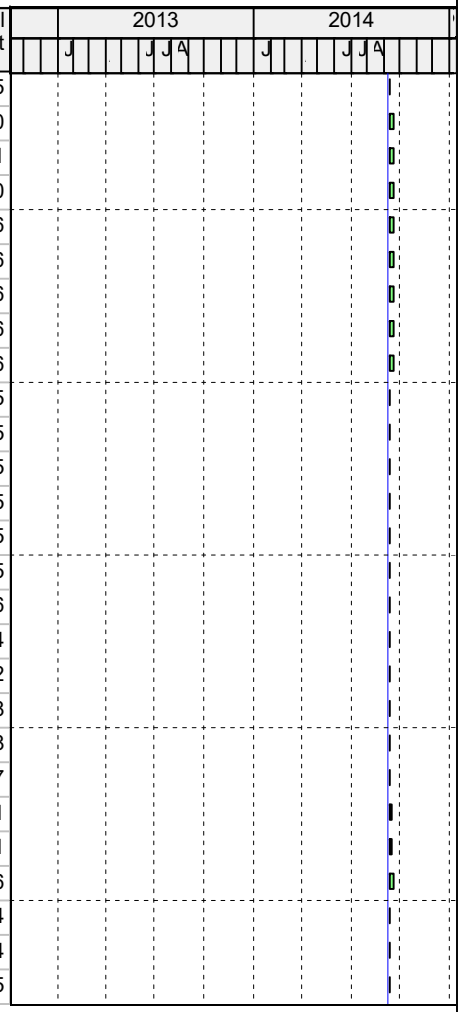



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7030 | Paint | 1 | 1 | 12-Sep-14 | 12-Sep-14 | 44 |
| L09-7130 | GWB Hang/Tape/Finish | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 45 |
| L10-7130 | GWB Hang/Tape/Finish | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 45 |
| L11-7130 | GWB Hang/Tape/Finish | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 45 |
| L12-7130 | GWB Hang/Tape/Finish | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 45 |
| L14-7130 | GWB Hang/Tape/Finish | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 45 |
| L15-7130 | GWB Hang/Tape/Finish | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 45 |
| L16-7130 | GWB Hang/Tape/Finish | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 46 |
| L17-7128 | Inspections for GWB Cover | 1 | 1 | 12-Sep-14 | 12-Sep-14 | 44 |
| L04-8138 | Install Toilet Accessories | 4 | 4 | 12-Sep-14 | 16-Sep-14 | 12 |
| L08-8136 | Install Counter Subtops | 3 | 3 | 12-Sep-14 | 16-Sep-14 | 39 |
| L10-8136 | Install Counter Subtops | 3 | 3 | 12-Sep-14 | 16-Sep-14 | 43 |
| LL2-6034 | LL2 - Electrical RI at Elevator Lobby | 2 | 2 | 12-Sep-14 | 15-Sep-14 | 35 |
| LL1-Z3-6032 | GWB Hang/Tape at Elevator Lobby | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 35 |
| L05-8200a | Install Guestroom Murals | 2 | 2 | 12-Sep-14 | 15-Sep-14 | 22 |
| L1-5104a | L1 - Measure/Fabricate Storefront Glazing | 15 | 15 | 12-Sep-14 | 02-Oct-14 | 18 |
| LL2E-8122 | LL2 - Hang GWB at Fire Pump Room | 3 | 3 | 12-Sep-14 | 16-Sep-14 | 37 |
| L03-8404 | Hang/Tape GWB at Elevator Lobby | 6 | 6 | 13-Sep-14 | 19-Sep-14 | 34 |
| L04-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 27 |
| L07-8402 | Electrical Rough-In at Elevator Lobby | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 40 |
| L08-8402 | Electrical Rough-In at Elevator Lobby | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 40 |
| L09-8402 | Electrical Rough-In at Elevator Lobby | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 41 |
| L10-8402 | Electrical Rough-In at Elevator Lobby | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 41 |
| L11-8402 | Electrical Rough-In at Elevator Lobby | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 75 |
| L05-8405 | Cover Inspection | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 28 |
| L06-8405 | Cover Inspection | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 42 |
| L07-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 40 |

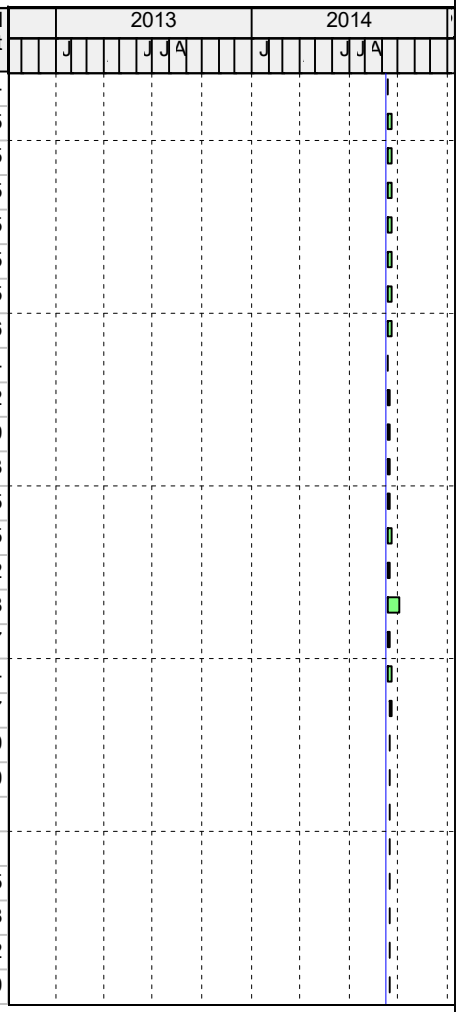



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 40 |
| L09-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 41 |
| L10-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 41 |
| L11-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 38 |
| L14-8395 | Framing at Elevator Lobby | 4 | 4 | 15-Sep-14 | 18-Sep-14 | 25 |
| L15-8395 | Framing at Elevator Lobby | 4 | 4 | 15-Sep-14 | 18-Sep-14 | 25 |
| MPP-1004 | Podium - Pool Area & Cornice | 5 | 5 | 15-Sep-14* | 19-Sep-14 | 0 |
| MPP-1006 | Podium - Install Level 3 Cornice (All 4 Sides) | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 57 |
| L06-8201 | Install ACT Grid @ Corridors | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 30 |
| L07-8201 | Install ACT Grid @ Corridors | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 32 |
| L08-8201 | Install ACT Grid @ Corridors | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 34 |
| L09-8201 | Install ACT Grid @ Corridors | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 36 |
| L10-8201 | Install ACT Grid @ Corridors | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 37 |
| L03-7032 | Install VCT Flooring (x42) | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 44 |
| L10-7032 | Install VCT Flooring (x42) | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 44 |
| L11-7034 | Install Door and Hardware (x42) | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 45 |
| L12-7032 | Install VCT Flooring (x42) | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 44 |
| L14-7030 | Paint | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 43 |
| L17-7130 | GWB Hang/Tape/Finish | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 44 |
| MPT-1018 | Tower - Install Roof Penthouse (Elev 36b,37,38.39) | 8 | 8 | 15-Sep-14 | 24-Sep-14 | 64 |
| MPT-1020 | Tower - Install E/W Wing, East End (Elev 41,44) | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 67 |
| LL1-Z2-8102a | GWB Hang (Ceilings) & Inspection | 9 | 9 | 15-Sep-14 | 25-Sep-14 | 19 |
| LL2-2048a | LL2 - Move in Laundry Room Ironer | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 46 |
| LL1-Z3-FCC18 | FCC - Install Temp Door | 1 | 1 | 15-Sep-14 | 15-Sep-14 | 38 |
| MPT-1018a | Tower - Install High Roof Cornice | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 67 |
| MPT-1018b | Tower - Install Level 17 Cornice | 3 | 3 | 15-Sep-14 | 17-Sep-14 | 64 |
| L05-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 16-Sep-14 | 20-Sep-14 | 33 |

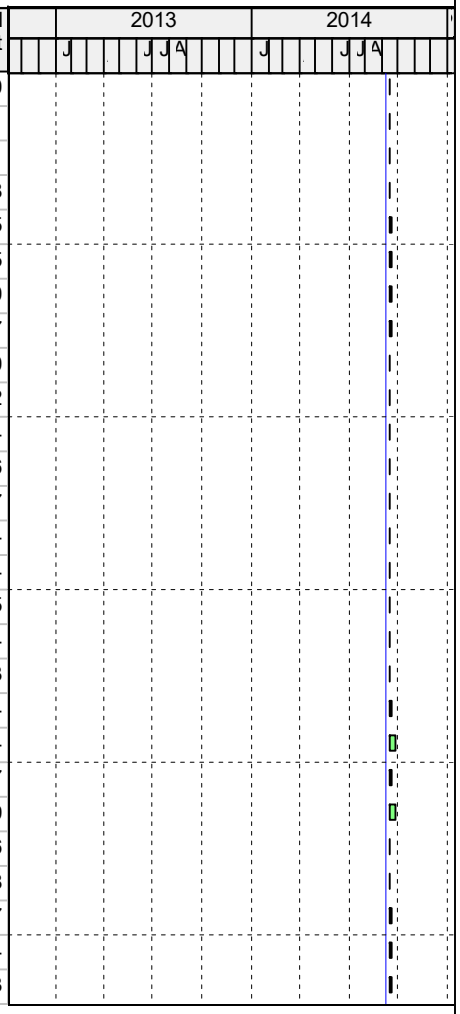



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8404 | Hang/Tape GWB at Elevator Lobby | 5 | 5 | 16-Sep-14 | 20-Sep-14 | 51 |
| L12-8402 | Electrical Rough-In at Elevator Lobby | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 36 |
| L12-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 36 |
| L16-8395 | Framing at Elevator Lobby | 4 | 4 | 16-Sep-14 | 19-Sep-14 | 25 |
| L17-8395 | Framing at Elevator Lobby | 4 | 4 | 16-Sep-14 | 19-Sep-14 | 25 |
| L03-7034 | Install Door and Hardware (x42) | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 44 |
| L03-7132 | Paint | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 48 |
| L04-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 48 |
| L05-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 51 |
| L06-7030 | Paint | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 42 |
| L07-7030 | Paint | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 42 |
| L08-7030 | Paint | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 42 |
| L09-7030 | Paint | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 42 |
| L10-7034 | Install Door and Hardware (x42) | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 44 |
| L11-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 16-Sep-14 | 18-Sep-14 | 45 |
| L12-7034 | Install Door and Hardware (x42) | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 44 |
| L14-7032 | Install VCT Flooring (x42) | 1 | 1 | 16-Sep-14 | 16-Sep-14 | 43 |
| MPT-1016 | Tower - Install N/S Wing, S. End W. of Manlift (Elev 2 | 6 | 6 | 16-Sep-14 | 23-Sep-14 | 65 |
| L11-8136 | Install Counter Subtops | 3 | 3 | 16-Sep-14 | 18-Sep-14 | 43 |
| L09-8136 | Install Counter Subtops | 3 | 3 | 16-Sep-14 | 18-Sep-14 | 39 |
| L06-8200a | Install Guestroom Murals | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 22 |
| LL1-Z3-FCC20 | FCC - Rough-In and Install Panels | 25 | 25 | 16-Sep-14 | 20-Oct-14 | 38 |
| L1BOH2-8100 | Insulation | 4 | 4 | 17-Sep-14 | 22-Sep-14 | 20 |
| L17-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 13 |
| L17-6040 | Test Heat Pumps - L16 and L17 | 3 | 3 | 17-Sep-14 | 19-Sep-14 | 10 |
| L17-6036 | Framing Around Heat Pump & Soffit | 3 | 3 | 17-Sep-14 | 19-Sep-14 | 10 |
| L07-8405 | Cover Inspection | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 40 |

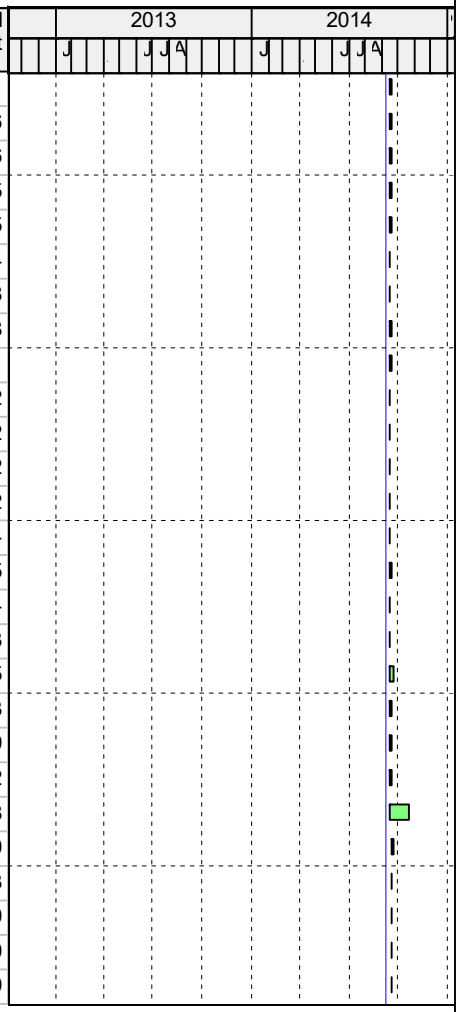



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8405 | Cover Inspection | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 40 |
| L09-8405 | Cover Inspection | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 41 |
| L10-8405 | Cover Inspection | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 41 |
| L11-8405 | Cover Inspection | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 38 |
| MPT-1012 | Tower - Install N/S Wing, S. End Concrete (Elev 33,34 | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 65 |
| L03-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 23 |
| L11-8201 | Install ACT Grid @ Corridors | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 37 |
| L03-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 17-Sep-14 | 19-Sep-14 | 44 |
| L03-7134 | Install VCT Flooring | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 48 |
| L06-7032 | Install VCT Flooring (x42) | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 42 |
| L07-7032 | Install VCT Flooring (x42) | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 42 |
| L08-7032 | Install VCT Flooring (x42) | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 42 |
| L09-7032 | Install VCT Flooring (x42) | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 42 |
| L10-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 17-Sep-14 | 19-Sep-14 | 44 |
| L12-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 17-Sep-14 | 19-Sep-14 | 44 |
| L14-7034 | Install Door and Hardware (x42) | 1 | 1 | 17-Sep-14 | 17-Sep-14 | 43 |
| L05-8138 | Install Toilet Accessories | 3 | 3 | 17-Sep-14 | 19-Sep-14 | 10 |
| L12-8136 | Install Counter Subtops | 3 | 3 | 17-Sep-14 | 19-Sep-14 | 44 |
| L1K-8102a | GWB Hang (Ceilings at Public Restroom) & Inspectio | 4 | 4 | 17-Sep-14 | 22-Sep-14 | 17 |
| L02-6025 | L2 - Framing Go-Back Work (left out for mechanical e | 4 | 4 | 17-Sep-14 | 22-Sep-14 | 27 |
| LL2-2058 | LL2 - Tape/Finish Laundry Room | 3 | 3 | 17-Sep-14 | 19-Sep-14 | 46 |
| LL2E-8124 | LL2 - Temp-In Louver Opening at Fire Pump Room | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 37 |
| L1BOH2-8102 | GWB Hang (Walls) | 5 | 5 | 18-Sep-14 | 23-Sep-14 | 24 |
| L07-8404 | Hang/Tape GWB at Elevator Lobby | 6 | 6 | 18-Sep-14 | 24-Sep-14 | 49 |
| L08-8404 | Hang/Tape GWB at Elevator Lobby | 6 | 6 | 18-Sep-14 | 25-Sep-14 | 40 |
| L09-8404 | Hang/Tape GWB at Elevator Lobby | 6 | 6 | 18-Sep-14 | 24-Sep-14 | 51 |
| L10-8404 | Hang/Tape GWB at Elevator Lobby | 6 | 6 | 18-Sep-14 | 24-Sep-14 | 51 |

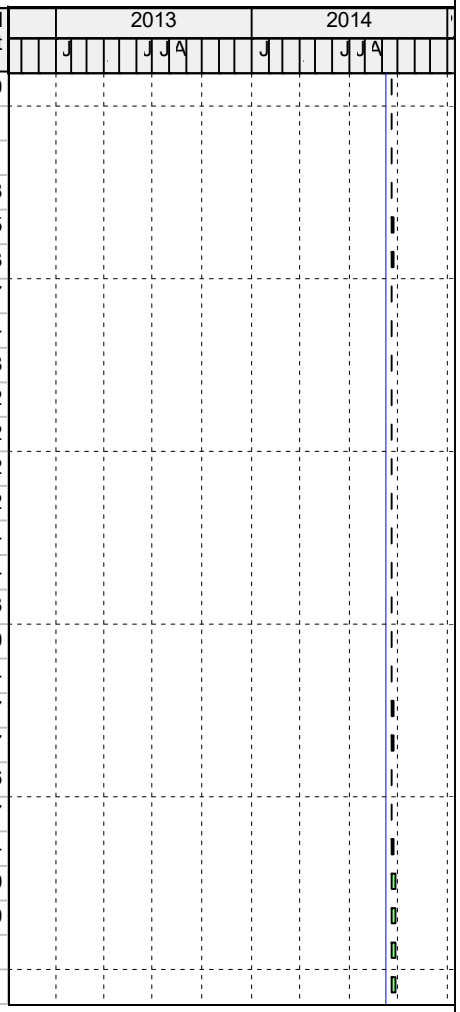



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8404 | Hang/Tape GWB at Elevator Lobby | 6 | 6 | 18-Sep-14 | 24-Sep-14 | 47 |
| L12-8405 | Cover Inspection | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 36 |
| L04-8129 | Install Shower Doors | 4 | 4 | 18-Sep-14 | 23-Sep-14 | 42 |
| L04-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 22 |
| L12-8201 | Install ACT Grid @ Corridors | 2 | 2 | 18-Sep-14 | 19-Sep-14 | 38 |
| L03-7136 | Install Door and Hardware | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 48 |
| L04-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 48 |
| L05-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 51 |
| L06-7034 | Install Door and Hardware (x42) | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 42 |
| L07-7034 | Install Door and Hardware (x42) | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 42 |
| L08-7034 | Install Door and Hardware (x42) | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 42 |
| L09-7034 | Install Door and Hardware (x42) | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 42 |
| L14-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 18-Sep-14 | 22-Sep-14 | 43 |
| L15-7030 | Paint | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 40 |
| L16-7030 | Paint | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 41 |
| L17-7030 | Paint | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 40 |
| L04-7132 | Paint | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 46 |
| L05-7132 | Paint | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 46 |
| L06-7132 | Paint | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 46 |
| L07-7132 | Paint | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 46 |
| L08-7132 | Paint | 1 | 1 | 18-Sep-14 | 18-Sep-14 | 46 |
| L03-8634 | Pool - Install reinforcing steel & inspect | 5 | 5 | 18-Sep-14 | 24-Sep-14 | 12 |
| L07-8200a | Install Guestroom Murals | 2 | 2 | 18-Sep-14 | 19-Sep-14 | 22 |
| L12-8404 | Hang/Tape GWB at Elevator Lobby | 6 | 6 | 19-Sep-14 | 25-Sep-14 | 45 |
| L14-8402 | Electrical Rough-In at Elevator Lobby | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 32 |
| L15-8402 | Electrical Rough-In at Elevator Lobby | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 27 |
| L14-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 32 |

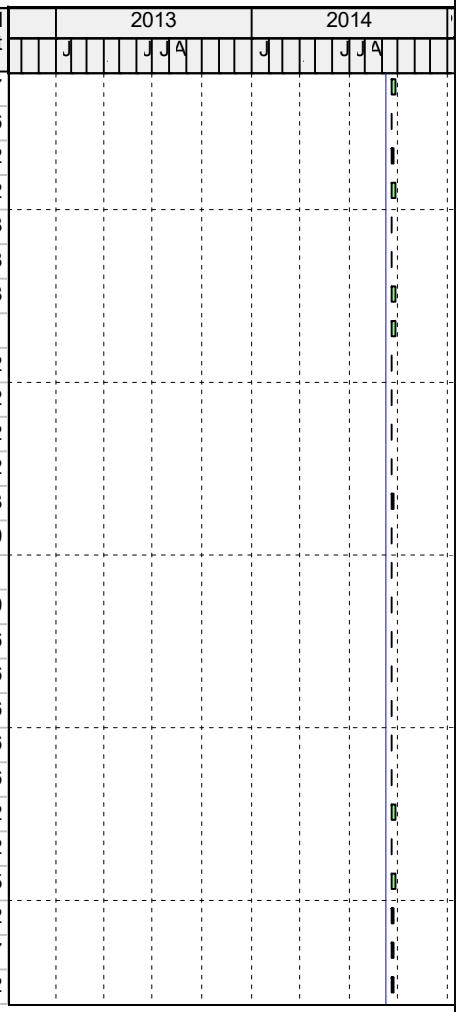



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 27 |
| L03-7138 | Electrical Trim-Out | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 48 |
| L06-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 19-Sep-14 | 23-Sep-14 | 42 |
| L07-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 19-Sep-14 | 23-Sep-14 | 42 |
| L08-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 19-Sep-14 | 23-Sep-14 | 42 |
| L09-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 19-Sep-14 | 23-Sep-14 | 42 |
| L11-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 45 |
| L15-7032 | Install VCT Flooring (x42) | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 40 |
| L16-7032 | Install VCT Flooring (x42) | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 41 |
| L17-7032 | Install VCT Flooring (x42) | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 40 |
| L04-7134 | Install VCT Flooring | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 46 |
| L05-7134 | Install VCT Flooring | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 46 |
| L06-7134 | Install VCT Flooring | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 46 |
| L07-7134 | Install VCT Flooring | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 46 |
| L08-7134 | Install VCT Flooring | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 46 |
| L09-7132 | Paint | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 45 |
| L10-7132 | Paint | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 45 |
| L11-7132 | Paint | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 45 |
| L12-7132 | Paint | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 45 |
| L14-7132 | Paint | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 45 |
| L15-7132 | Paint | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 45 |
| L16-7132 | Paint | 1 | 1 | 19-Sep-14 | 19-Sep-14 | 46 |
| L17-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 10 |
| L03-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 22-Sep-14 | 24-Sep-14 | 28 |
| L04-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 22-Sep-14 | 24-Sep-14 | 27 |
| L05-8406 | Paint Prime/1st Coat at Elevator Lobby | 2 | 2 | 22-Sep-14 | 23-Sep-14 | 28 |
| L06-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 22-Sep-14 | 24-Sep-14 | 42 |

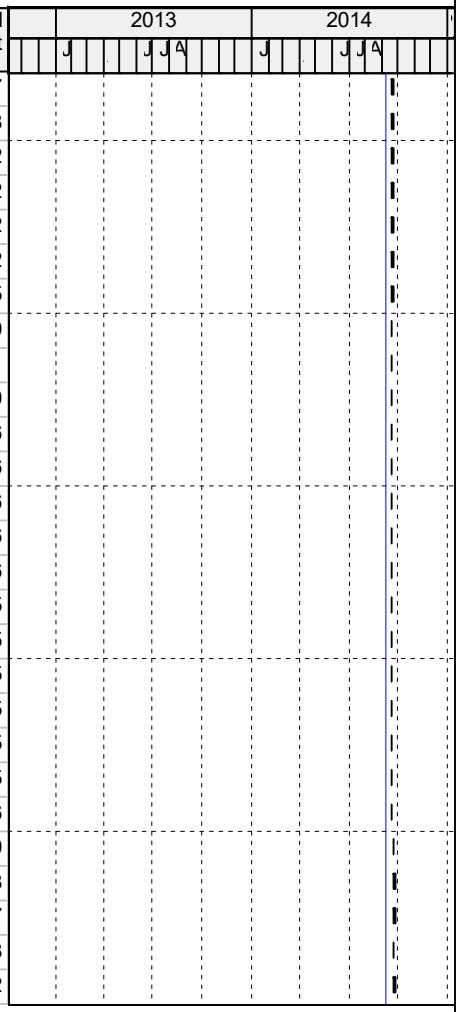



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8402 | Electrical Rough-In at Elevator Lobby | 2 | 2 | 22-Sep-14 | 23-Sep-14 | 26 |
| L17-8402 | Electrical Rough-In at Elevator Lobby | 2 | 2 | 22-Sep-14 | 23-Sep-14 | 25 |
| LL1-6014lb | L1 bar redesign - rework ceiling framing & inspection | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 17 |
| L16-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 2 | 22-Sep-14 | 23-Sep-14 | 26 |
| L17-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 2 | 22-Sep-14 | 23-Sep-14 | 25 |
| MPP-1010 | Podium - Install East Elevation (Elev 5 & 7) | 10 | 10 | 22-Sep-14 | 03-Oct-14 | 57 |
| L03-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 22-Sep-14 | 23-Sep-14 | 44 |
| L10-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 22-Sep-14 | 23-Sep-14 | 44 |
| L12-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 22-Sep-14 | 23-Sep-14 | 44 |
| L15-7034 | Install Door and Hardware (x42) | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 40 |
| L16-7034 | Install Door and Hardware (x42) | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 41 |
| L17-7034 | Install Door and Hardware (x42) | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 40 |
| L04-7136 | Install Door and Hardware | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 46 |
| L05-7136 | Install Door and Hardware | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 46 |
| L06-7136 | Install Door and Hardware | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 46 |
| L07-7136 | Install Door and Hardware | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 46 |
| L08-7136 | Install Door and Hardware | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 46 |
| L09-7134 | Install VCT Flooring | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 45 |
| L10-7134 | Install VCT Flooring | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 45 |
| L11-7134 | Install VCT Flooring | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 45 |
| L12-7134 | Install VCT Flooring | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 45 |
| L14-7134 | Install VCT Flooring | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 45 |
| L15-7134 | Install VCT Flooring | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 45 |
| L16-7134 | Install VCT Flooring | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 46 |
| L17-7132 | Paint | 1 | 1 | 22-Sep-14 | 22-Sep-14 | 44 |
| L06-8138 | Install Toilet Accessories | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 10 |
| L14-8136 | Install Counter Subtops | 3 | 3 | 22-Sep-14 | 24-Sep-14 | 43 |

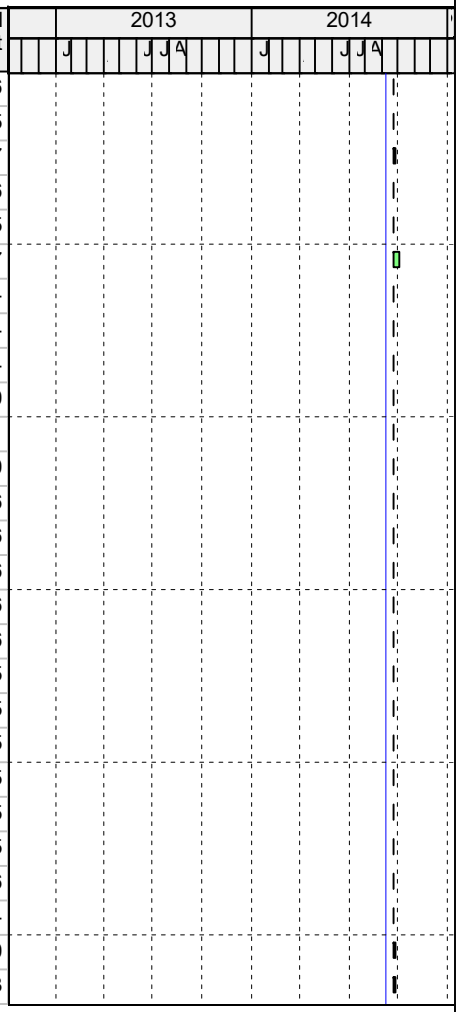



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2060 | LL2 - Paint Prime/First Coat at Laundry Room | 2 | 2 | 22-Sep-14 | 23-Sep-14 | 46 |
| L08-8200a | Install Guestroom Murals | 2 | 2 | 22-Sep-14 | 23-Sep-14 | 22 |
| L3-5104a | L3 - Measure/Fabricate Storefront Glazing | 15 | 15 | 22-Sep-14 | 10-Oct-14 | 18 |
| LL3-8102a | LL3 - GWB Tape/Finish | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 30 |
| L14-8405 | Cover Inspection | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 32 |
| L15-8405 | Cover Inspection | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 27 |
| L05-8129 | Install Shower Doors | 4 | 4 | 23-Sep-14 | 26-Sep-14 | 42 |
| L14-8201 | Install ACT Grid @ Corridors | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 36 |
| L03-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 48 |
| L11-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 45 |
| L14-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 43 |
| L15-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 23-Sep-14 | 25-Sep-14 | 40 |
| L16-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 23-Sep-14 | 25-Sep-14 | 41 |
| L17-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 23-Sep-14 | 25-Sep-14 | 40 |
| L04-7138 | Electrical Trim-Out | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 46 |
| L05-7138 | Electrical Trim-Out | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 46 |
| L06-7138 | Electrical Trim-Out | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 46 |
| L07-7138 | Electrical Trim-Out | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 46 |
| L08-7138 | Electrical Trim-Out | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 46 |
| L09-7136 | Install Door and Hardware | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 45 |
| L10-7136 | Install Door and Hardware | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 45 |
| L11-7136 | Install Door and Hardware | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 45 |
| L12-7136 | Install Door and Hardware | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 45 |
| L14-7136 | Install Door and Hardware | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 45 |
| L15-7136 | Install Door and Hardware | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 45 |
| L16-7136 | Install Door and Hardware | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 46 |
| L17-7134 | Install VCT Flooring | 1 | 1 | 23-Sep-14 | 23-Sep-14 | 44 |

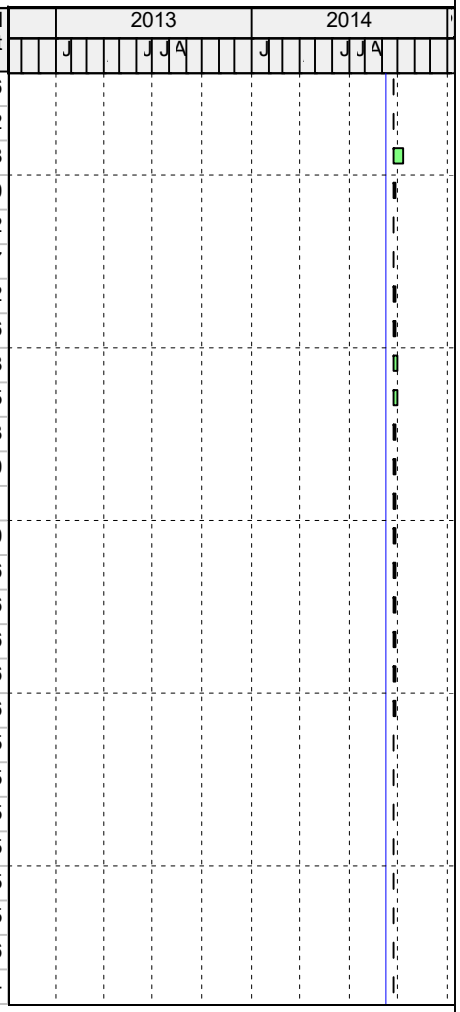



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1BOH2-8215 | GWB Tape (Walls) | 3 | 3 | 24-Sep-14 | 26-Sep-14 | 20 |
| L03-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 28 |
| L04-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 27 |
| L05-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 28 |
| L14-8404 | Hang/Tape GWB at Elevator Lobby | 6 | 6 | 24-Sep-14 | 30-Sep-14 | 38 |
| L15-8404 | Hang/Tape GWB at Elevator Lobby | 6 | 6 | 24-Sep-14 | 01-Oct-14 | 27 |
| LL2-2048 | LL2 - Set Laundry Room equipment (BY OTHERS) | 3 | 3 | 24-Sep-14 | 26-Sep-14 | 46 |
| L16-8405 | Cover Inspection | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 26 |
| L17-8405 | Cover Inspection | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 25 |
| L05-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 24-Sep-14 | 29-Sep-14 | 29 |
| L03-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 44 |
| L06-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 42 |
| L07-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 42 |
| L08-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 42 |
| L09-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 42 |
| L10-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 44 |
| L12-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 44 |
| L09-7138 | Electrical Trim-Out | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 45 |
| L10-7138 | Electrical Trim-Out | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 45 |
| L11-7138 | Electrical Trim-Out | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 45 |
| L12-7138 | Electrical Trim-Out | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 45 |
| L14-7138 | Electrical Trim-Out | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 45 |
| L15-7138 | Electrical Trim-Out | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 45 |
| L16-7138 | Electrical Trim-Out | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 46 |
| L17-7136 | Install Door and Hardware | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 44 |
| L04-8412 | Final Coat Finish Paint at Elevator Lobby | 3 | 3 | 25-Sep-14 | 27-Sep-14 | 33 |
| L06-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 42 |

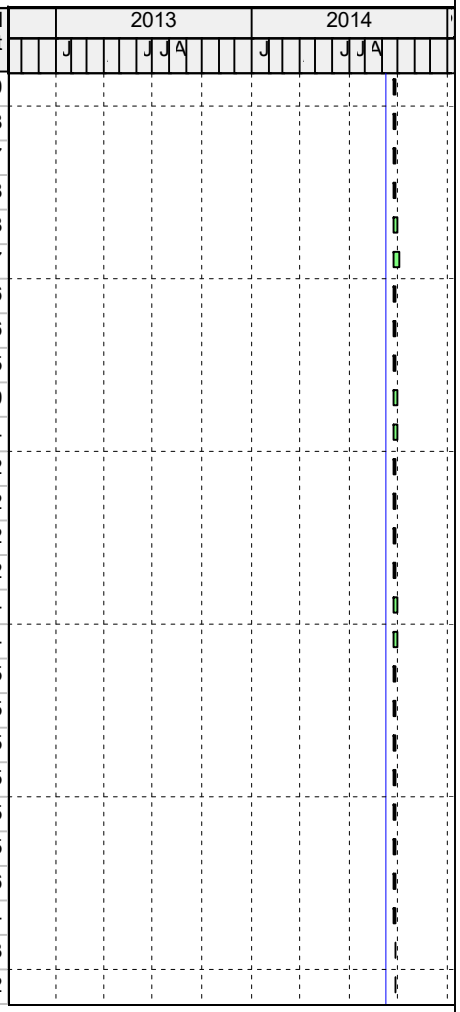



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 25-Sep-14 | 27-Sep-14 | 49 |
| L09-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 25-Sep-14 | 27-Sep-14 | 51 |
| L10-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 25-Sep-14 | 27-Sep-14 | 51 |
| L11-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 25-Sep-14 | 29-Sep-14 | 38 |
| L16-8404 | Hang/Tape GWB at Elevator Lobby | 6 | 6 | 25-Sep-14 | 02-Oct-14 | 26 |
| L17-8404 | Hang/Tape GWB at Elevator Lobby | 6 | 6 | 25-Sep-14 | 02-Oct-14 | 25 |
| L06-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 25-Sep-14 | 30-Sep-14 | 26 |
| L04-7042 | Install Tile Flooring (x41) | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 48 |
| L05-7042 | Install Tile Flooring (x41) | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 51 |
| L14-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 43 |
| L04-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 46 |
| L05-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 46 |
| L06-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 46 |
| L07-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 46 |
| L08-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 46 |
| L17-7138 | Electrical Trim-Out | 2 | 2 | 25-Sep-14 | 26-Sep-14 | 44 |
| L03-8636 | Pool - Shotcrete | 1 | 1 | 25-Sep-14 | 25-Sep-14 | 12 |
| L15-8136 | Install Counter Subtops | 3 | 3 | 25-Sep-14 | 29-Sep-14 | 42 |
| L02-6016a | L2 - Electrical Room Buildout | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 48 |
| LL1-Z3-FCC22 | FCC - Finishes | 10 | 10 | 25-Sep-14 | 08-Oct-14 | 46 |
| L03-8412 | Final Coat Finish Paint at Elevator Lobby | 3 | 3 | 26-Sep-14 | 29-Sep-14 | 34 |
| L05-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 26-Sep-14 | 27-Sep-14 | 34 |
| L08-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 26-Sep-14 | 29-Sep-14 | 50 |
| L12-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 26-Sep-14 | 30-Sep-14 | 36 |
| L02-5104 | L2 - Storefront Glazing | 2 | 2 | 26-Sep-14 | 29-Sep-14 | 32 |
| L15-8201 | Install ACT Grid @ Corridors | 2 | 2 | 26-Sep-14 | 29-Sep-14 | 23 |
| L06-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 42 |

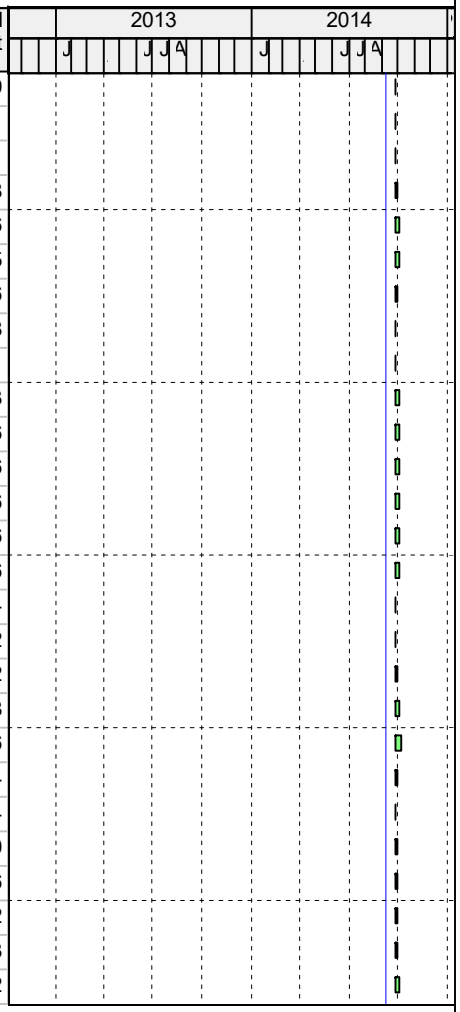



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 42 |
| L08-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 42 |
| L09-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 42 |
| L15-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 26-Sep-14 | 29-Sep-14 | 40 |
| L16-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 26-Sep-14 | 29-Sep-14 | 41 |
| L17-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 26-Sep-14 | 29-Sep-14 | 40 |
| L09-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 45 |
| L10-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 45 |
| L11-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 45 |
| L12-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 45 |
| L14-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 45 |
| L15-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 45 |
| L16-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 26-Sep-14 | 02-Oct-14 | 46 |
| L07-8138 | Install Toilet Accessories | 4 | 4 | 26-Sep-14 | 01-Oct-14 | 10 |
| LL1-8102a | GWB Hang/Tape (Ceilings) | 10 | 10 | 26-Sep-14 | 07-Oct-14 | 20 |
| LL2-8106a | LL2 - Pinned Insulation @ Ramp Ceiling | 4 | 4 | 26-Sep-14 | 01-Oct-14 | 35 |
| L04-8206a | Install Base @ Corridors | 3 | 3 | 26-Sep-14 | 30-Sep-14 | 47 |
| L1BOH2-8104 | Prime Paint | 2 | 2 | 27-Sep-14 | 29-Sep-14 | 24 |
| L06-8412 | Final Coat Finish Paint at Elevator Lobby | 3 | 3 | 27-Sep-14 | 30-Sep-14 | 52 |
| L1BOH2-8114 | T Bar Grid Ceiling | 3 | 3 | 29-Sep-14 | 01-Oct-14 | 20 |
| L03-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 29-Sep-14 | 01-Oct-14 | 29 |
| L04-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 29-Sep-14 | 01-Oct-14 | 28 |
| L05-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 29-Sep-14 | 01-Oct-14 | 29 |
| L05-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 29-Sep-14 | 29-Sep-14 | 31 |
| L07-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 39 |
| L08-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 41 |
| L09-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 41 |

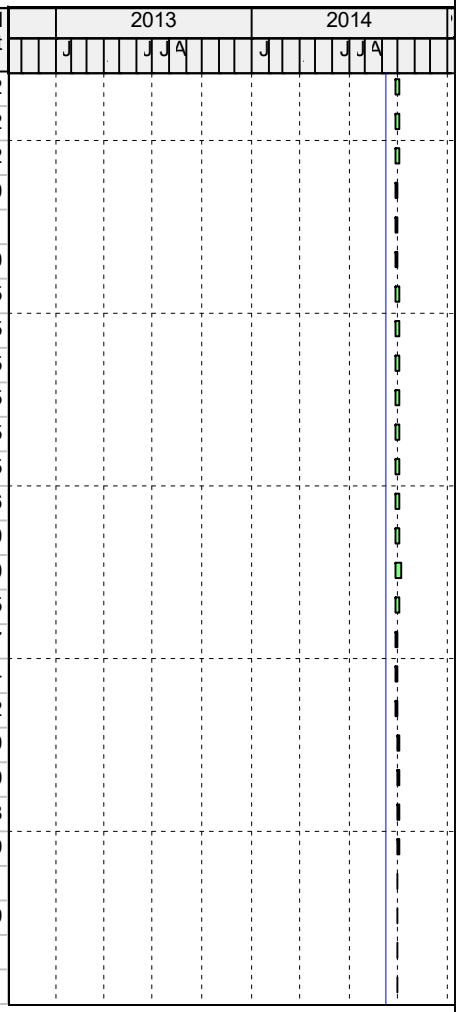



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 41 |
| LL2-2050 | LL2 - Laundry Room equipment final connections (MI | 4 | 4 | 29-Sep-14 | 02-Oct-14 | 46 |
| MPP-1000 | Podium - Install W/S/N Elevations (Elev 1-5, 6,9-19,2 | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 57 |
| L06-8129 | Install Shower Doors | 4 | 4 | 29-Sep-14 | 02-Oct-14 | 38 |
| L04-7044 | Install Vending Cabinets (x41) | 1 | 1 | 29-Sep-14 | 29-Sep-14 | 48 |
| L05-7044 | Install Vending Cabinets (x41) | 1 | 1 | 29-Sep-14 | 29-Sep-14 | 55 |
| L17-7140 | Fire Alarm / Elec Specialties Trim-Out | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 44 |
| LL1-6014lb2 | L1 bar redesign - GWB hang at ceilings | 4 | 4 | 29-Sep-14 | 02-Oct-14 | 17 |
| I-1102 | Additional work at new L17 guest rooms | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 10 |
| L03-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 30-Sep-14 | 30-Sep-14 | 30 |
| L11-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 30-Sep-14 | 01-Oct-14 | 38 |
| L07-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 24 |
| L11-7042 | Install Tile Flooring (x41) | 2 | 2 | 30-Sep-14 | 01-Oct-14 | 45 |
| L15-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 40 |
| L16-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 41 |
| L17-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 40 |
| L05-8206a | Install Base @ Corridors | 3 | 3 | 30-Sep-14 | 02-Oct-14 | 45 |
| L03-8418 | Flooring at Elevator Lobby | 3 | 3 | 01-Oct-14 | 03-Oct-14 | 53 |
| L04-8418 | Flooring at Elevator Lobby | 3 | 3 | 01-Oct-14 | 03-Oct-14 | 43 |
| L05-8418 | Flooring at Elevator Lobby | 3 | 3 | 01-Oct-14 | 03-Oct-14 | 53 |
| L06-8414 | Elec Trim / Finish at Elevator Lobby | 2 | 2 | 01-Oct-14 | 02-Oct-14 | 43 |
| L06-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 01-Oct-14 | 01-Oct-14 | 43 |
| L07-8412 | Final Coat Finish Paint at Elevator Lobby | 3 | 3 | 01-Oct-14 | 03-Oct-14 | 39 |
| L08-8412 | Final Coat Finish Paint at Elevator Lobby | 3 | 3 | 01-Oct-14 | 03-Oct-14 | 41 |
| L09-8412 | Final Coat Finish Paint at Elevator Lobby | 3 | 3 | 01-Oct-14 | 03-Oct-14 | 41 |
| L10-8412 | Final Coat Finish Paint at Elevator Lobby | 3 | 3 | 01-Oct-14 | 03-Oct-14 | 41 |
| L12-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 01-Oct-14 | 02-Oct-14 | 36 |

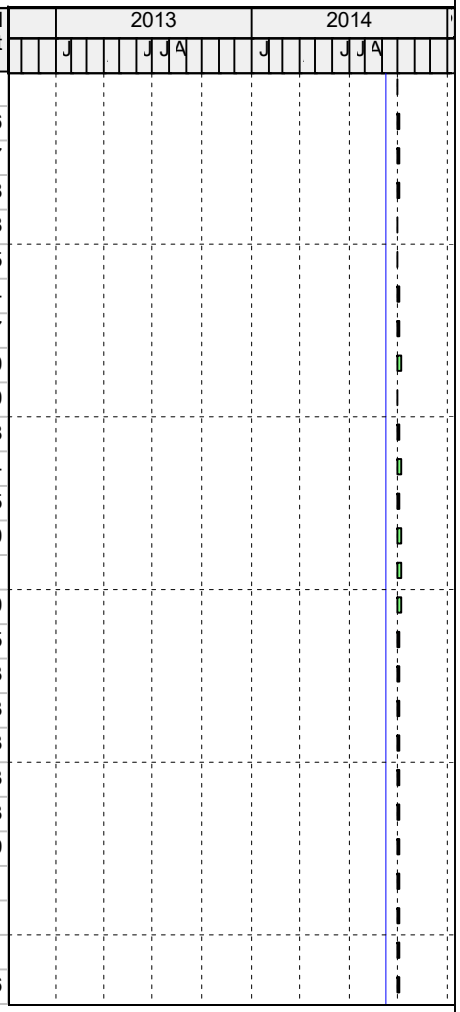



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 01-Oct-14 | 03-Oct-14 | 31 |
| L08-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 01-Oct-14 | 07-Oct-14 | 22 |
| L03-7042 | Install Tile Flooring (x41) | 2 | 2 | 01-Oct-14 | 02-Oct-14 | 44 |
| L10-7042 | Install Tile Flooring (x41) | 2 | 2 | 01-Oct-14 | 02-Oct-14 | 44 |
| L12-7042 | Install Tile Flooring (x41) | 2 | 2 | 01-Oct-14 | 02-Oct-14 | 44 |
| L04-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 28 |
| L06-8418 | Flooring at Elevator Lobby | 3 | 3 | 02-Oct-14 | 04-Oct-14 | 52 |
| L08-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 42 |
| L10-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 42 |
| L11-8412 | Final Coat Finish Paint at Elevator Lobby | 3 | 3 | 02-Oct-14 | 06-Oct-14 | 38 |
| L15-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 02-Oct-14 | 06-Oct-14 | 27 |
| L11-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 02-Oct-14 | 02-Oct-14 | 45 |
| L14-7042 | Install Tile Flooring (x41) | 2 | 2 | 02-Oct-14 | 03-Oct-14 | 43 |
| L08-8138 | Install Toilet Accessories | 4 | 4 | 02-Oct-14 | 07-Oct-14 | 10 |
| L1BOH2C-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 5 | 5 | 02-Oct-14 | 08-Oct-14 | 20 |
| L1BOH2C-6014 | Complete Plumbing RI @ Ceilings & Inspection | 5 | 5 | 02-Oct-14 | 08-Oct-14 | 20 |
| L1BOH2C-6016 | Complete Electrical RI @ Ceilings & Inspection | 5 | 5 | 02-Oct-14 | 08-Oct-14 | 20 |
| L1BOH2C-6018 | Complete HVAC RI @ Ceilings & Inspection | 5 | 5 | 02-Oct-14 | 08-Oct-14 | 20 |
| L1BOH2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 5 | 02-Oct-14 | 08-Oct-14 | 20 |
| LL2-2062 | LL2 - Connect Eye Wash and Sinks at Laundry Roon | 2 | 2 | 02-Oct-14 | 03-Oct-14 | 46 |
| L03-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 03-Oct-14 | 04-Oct-14 | 53 |
| L04-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 03-Oct-14 | 06-Oct-14 | 43 |
| L05-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 03-Oct-14 | 04-Oct-14 | 53 |
| L08-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Oct-14 | 06-Oct-14 | 50 |
| L09-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Oct-14 | 07-Oct-14 | 41 |
| L09-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 41 |
| L10-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Oct-14 | 07-Oct-14 | 41 |

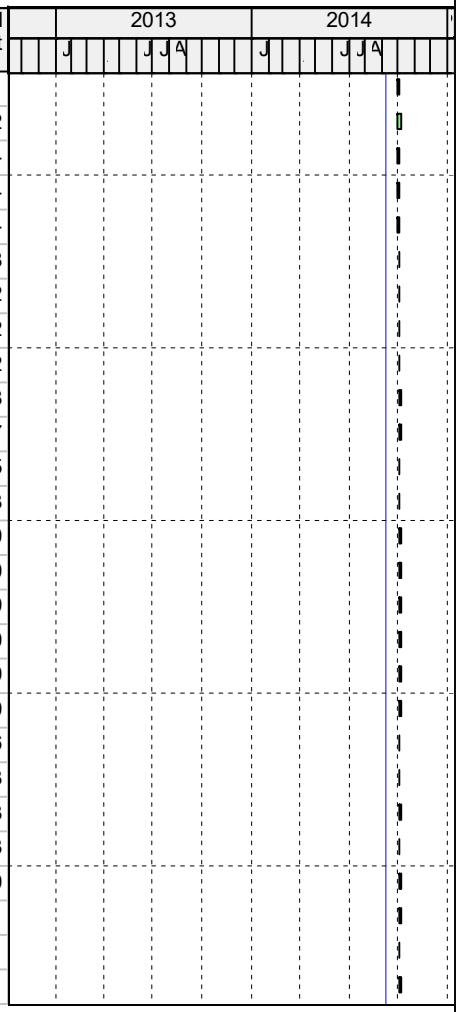



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Oct-14 | 07-Oct-14 | 38 |
| L12-8412 | Final Coat Finish Paint at Elevator Lobby | 3 | 3 | 03-Oct-14 | 07-Oct-14 | 36 |
| L16-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 03-Oct-14 | 07-Oct-14 | 26 |
| L17-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 03-Oct-14 | 07-Oct-14 | 25 |
| L07-8129 | Install Shower Doors | 4 | 4 | 03-Oct-14 | 08-Oct-14 | 38 |
| L03-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 44 |
| L06-7042 | Install Tile Flooring (x41) | 2 | 2 | 03-Oct-14 | 06-Oct-14 | 42 |
| L07-7042 | Install Tile Flooring (x41) | 2 | 2 | 03-Oct-14 | 06-Oct-14 | 42 |
| L08-7042 | Install Tile Flooring (x41) | 2 | 2 | 03-Oct-14 | 06-Oct-14 | 42 |
| L09-7042 | Install Tile Flooring (x41) | 2 | 2 | 03-Oct-14 | 06-Oct-14 | 42 |
| L10-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 44 |
| L12-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 03-Oct-14 | 03-Oct-14 | 44 |
| L06-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 04-Oct-14 | 06-Oct-14 | 52 |
| L08-8418 | Flooring at Elevator Lobby | 3 | 3 | 04-Oct-14 | 07-Oct-14 | 50 |
| L09-8418 | Flooring at Elevator Lobby | 3 | 3 | 04-Oct-14 | 07-Oct-14 | 50 |
| L10-8418 | Flooring at Elevator Lobby | 3 | 3 | 04-Oct-14 | 07-Oct-14 | 50 |
| L10-8129 | Install Shower Doors | 4 | 4 | 04-Oct-14 | 08-Oct-14 | 25 |
| L07-8414 | Elec Trim / Finish at Elevator Lobby | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 39 |
| L11-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 38 |
| L14-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 31 |
| L14-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 43 |
| L08-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 41 |
| L09-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 41 |
| L10-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 41 |
| L11-8418 | Flooring at Elevator Lobby | 3 | 3 | 07-Oct-14 | 09-Oct-14 | 38 |
| L15-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 27 |
| L1K-8340 | Install walk-in cooler/freezer (BY OTHERS) | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 12 |

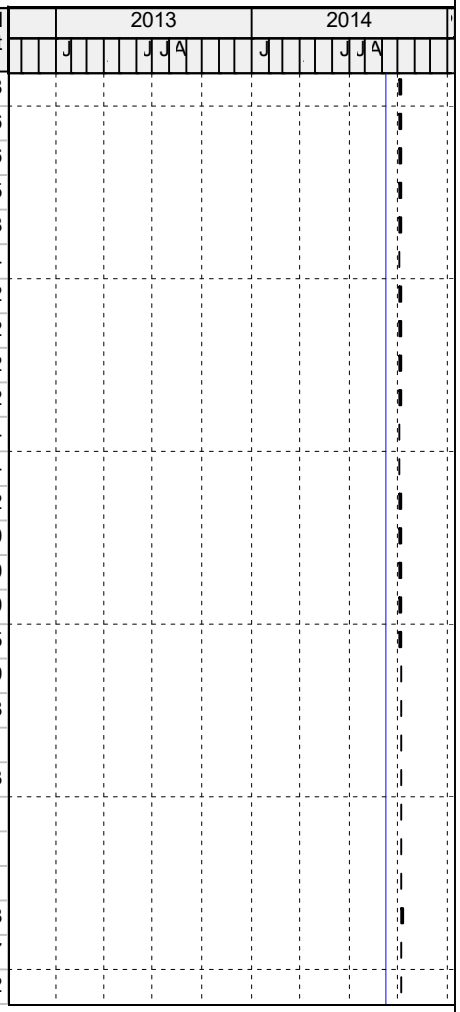



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 24 |
| L06-7044 | Install Vending Cabinets (x41) | 1 | 1 | 07-Oct-14 | 07-Oct-14 | 42 |
| L07-7044 | Install Vending Cabinets (x41) | 1 | 1 | 07-Oct-14 | 07-Oct-14 | 42 |
| L08-7044 | Install Vending Cabinets (x41) | 1 | 1 | 07-Oct-14 | 07-Oct-14 | 42 |
| L09-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 07-Oct-14 | 07-Oct-14 | 42 |
| L15-7042 | Install Tile Flooring (x41) | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 40 |
| L16-7042 | Install Tile Flooring (x41) | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 41 |
| L17-7042 | Install Tile Flooring (x41) | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 40 |
| LL4-6026 | LL4 - Set Elevator Fronts (Cars 1-4) | 1 | 1 | 07-Oct-14 | 07-Oct-14 | 17 |
| L07-8418 | Flooring at Elevator Lobby | 3 | 3 | 08-Oct-14 | 10-Oct-14 | 47 |
| L12-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 08-Oct-14 | 10-Oct-14 | 57 |
| L12-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 36 |
| L14-8412 | Final Coat Finish Paint at Elevator Lobby | 3 | 3 | 08-Oct-14 | 10-Oct-14 | 31 |
| L16-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 08-Oct-14 | 09-Oct-14 | 26 |
| L17-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 08-Oct-14 | 09-Oct-14 | 25 |
| L1K-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 08-Oct-14 | 09-Oct-14 | 12 |
| L10-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 08-Oct-14 | 14-Oct-14 | 22 |
| L09-8138 | Install Toilet Accessories | 4 | 4 | 08-Oct-14 | 13-Oct-14 | 10 |
| L16-8136 | Install Counter Subtops | 3 | 3 | 08-Oct-14 | 10-Oct-14 | 35 |
| LL4-6028 | LL4 - Frame Elevator Lobby | 2 | 2 | 08-Oct-14 | 09-Oct-14 | 17 |
| L1BOH2-8140 | Acoustical Ceiling Tile | 4 | 4 | 09-Oct-14 | 14-Oct-14 | 20 |
| L12-8418 | Flooring at Elevator Lobby | 3 | 3 | 09-Oct-14 | 13-Oct-14 | 36 |
| L15-8412 | Final Coat Finish Paint at Elevator Lobby | 3 | 3 | 09-Oct-14 | 13-Oct-14 | 27 |
| L08-8129 | Install Shower Doors | 4 | 4 | 09-Oct-14 | 14-Oct-14 | 34 |
| L16-8201 | Install ACT Grid @ Corridors | 2 | 2 | 09-Oct-14 | 10-Oct-14 | 15 |
| L15-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 40 |
| L16-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 41 |

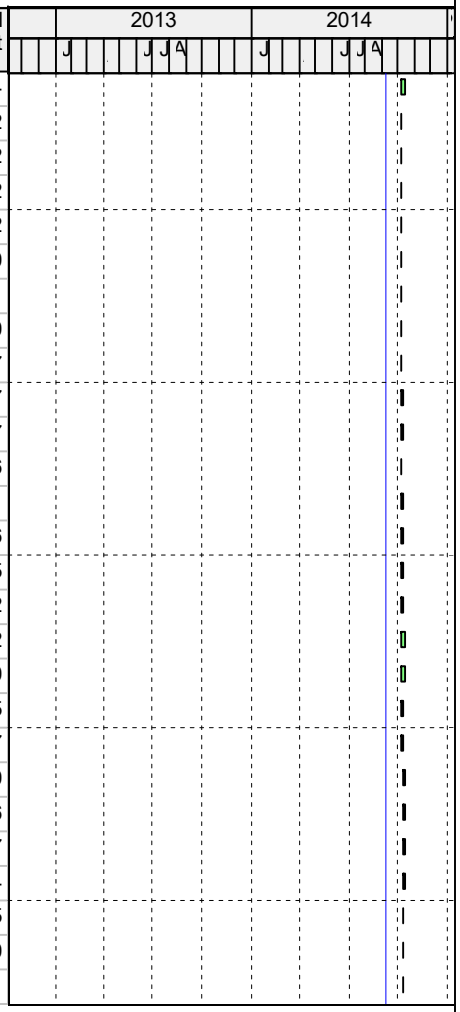



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 40 |
| L06-8206a | Install Base @ Corridors | 3 | 3 | 09-Oct-14 | 13-Oct-14 | 38 |
| L07-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 10-Oct-14 | 11-Oct-14 | 47 |
| L11-8408 | Install Wood Base at Elevator Lobby | 3 | 3 | 10-Oct-14 | 13-Oct-14 | 46 |
| L16-8412 | Final Coat Finish Paint at Elevator Lobby | 3 | 3 | 10-Oct-14 | 14-Oct-14 | 26 |
| L17-8412 | Final Coat Finish Paint at Elevator Lobby | 3 | 3 | 10-Oct-14 | 14-Oct-14 | 25 |
| L11-8129 | Install Shower Doors | 4 | 4 | 10-Oct-14 | 15-Oct-14 | 20 |
| LL4-6030 | LL4 - Electrical RI at Elevator Lobby | 2 | 2 | 10-Oct-14 | 13-Oct-14 | 17 |
| L14-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 31 |
| L14-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 13-Oct-14 | 13-Oct-14 | 33 |
| L07-8206a | Install Base @ Corridors | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 36 |
| L12-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 44 |
| L15-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 14-Oct-14 | 16-Oct-14 | 27 |
| L15-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 14-Oct-14 | 14-Oct-14 | 29 |
| L11-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 24 |
| L10-8138 | Install Toilet Accessories | 4 | 4 | 14-Oct-14 | 17-Oct-14 | 10 |
| L1B-8102a | GWB Hang/Tape (Ceilings) | 12 | 12 | 14-Oct-14 | 29-Oct-14 | 3 |
| L1BOH2-8200 | First Coat Finish Paint | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 20 |
| L16-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 15-Oct-14 | 17-Oct-14 | 26 |
| L16-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 15-Oct-14 | 15-Oct-14 | 28 |
| L17-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 15-Oct-14 | 17-Oct-14 | 25 |
| L17-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 15-Oct-14 | 15-Oct-14 | 28 |
| L09-8129 | Install Shower Doors | 4 | 4 | 15-Oct-14 | 18-Oct-14 | 41 |
| L12-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 22 |
| L17-8136 | Install Counter Subtops | 3 | 3 | 15-Oct-14 | 17-Oct-14 | 32 |
| L14-8418 | Flooring at Elevator Lobby | 3 | 3 | 16-Oct-14 | 20-Oct-14 | 31 |
| L12-8129 | Install Shower Doors | 4 | 4 | 16-Oct-14 | 21-Oct-14 | 16 |

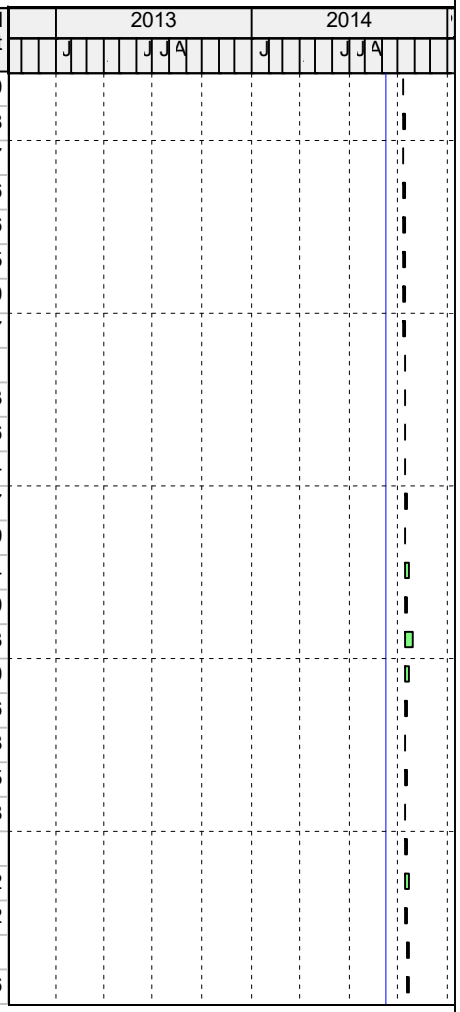



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8201 | Install ACT Grid @ Corridors | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 10 |
| L15-8418 | Flooring at Elevator Lobby | 3 | 3 | 17-Oct-14 | 21-Oct-14 | 30 |
| L03-8638 | Pool - Install pool deck and ADA lift | 3 | 3 | 17-Oct-14 | 21-Oct-14 | 12 |
| L08-8206a | Install Base @ Corridors | 3 | 3 | 17-Oct-14 | 21-Oct-14 | 35 |
| L16-8418 | Flooring at Elevator Lobby | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 30 |
| L17-8418 | Flooring at Elevator Lobby | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 29 |
| L11-8138 | Install Toilet Accessories | 4 | 4 | 20-Oct-14 | 23-Oct-14 | 10 |
| L14-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 21-Oct-14 | 22-Oct-14 | 38 |
| L03-8606 | L3 Pool - HVAC R/I | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 12 |
| L14-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 21-Oct-14 | 27-Oct-14 | 24 |
| L09-8206a | Install Base @ Corridors | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 34 |
| L1BOH2-8124 | Flooring | 4 | 4 | 22-Oct-14 | 27-Oct-14 | 20 |
| L15-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 22-Oct-14 | 23-Oct-14 | 30 |
| L14-8129 | Install Shower Doors | 4 | 4 | 22-Oct-14 | 27-Oct-14 | 16 |
| L15-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 22 |
| L03-8640 | Pool - Prep and install plaster | 2 | 2 | 22-Oct-14 | 23-Oct-14 | 12 |
| L16-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 30 |
| L17-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 29 |
| L1L-8102a | GWB Hang/Tape (Ceilings) | 11 | 11 | 23-Oct-14 | 06-Nov-14 | 0 |
| LL4-8102a | LL4 - GWB Tape/Finish | 4 | 4 | 23-Oct-14 | 28-Oct-14 | 17 |
| L03-8612 | L3 Pool - GWB hang/tape/finish | 5 | 5 | 24-Oct-14 | 30-Oct-14 | 12 |
| L03-8642 | Pool - Fill pool | 2 | 2 | 24-Oct-14 | 27-Oct-14 | 38 |
| L12-8138 | Install Toilet Accessories | 4 | 4 | 24-Oct-14 | 29-Oct-14 | 10 |
| LL1-Z2-8124a | Install Base | 3 | 3 | 24-Oct-14 | 28-Oct-14 | 19 |
| L1K-8124a | Install Flooring (Epoxy) | 8 | 8 | 24-Oct-14 | 01-Nov-14 | 16 |
| LL1-Z2-8108 | Install Junior Balllroom ceiling feature (allowance) | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 19 |
| L1BOH2-8124a | Install Base | 3 | 3 | 27-Oct-14 | 29-Oct-14 | 20 |

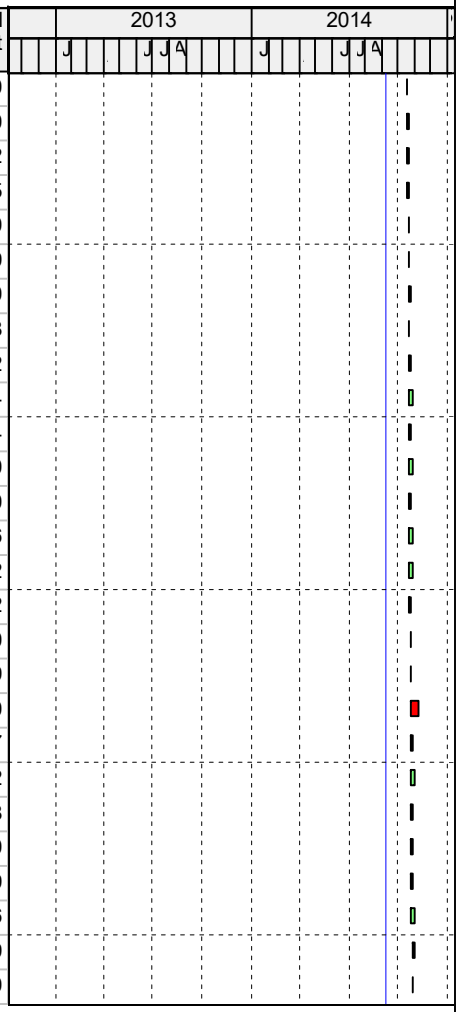



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8129 | Install Shower Doors | 4 | 4 | 28-Oct-14 | 31-Oct-14 | 16 |
| L16-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 28-Oct-14 | 03-Nov-14 | 24 |
| L03-8644 | Pool - Start-up and adjust pool equipment | 2 | 2 | 28-Oct-14 | 29-Oct-14 | 38 |
| L14-8138 | Install Toilet Accessories | 4 | 4 | 28-Oct-14 | 31-Oct-14 | 10 |
| L10-8206a | Install Base @ Corridors | 3 | 3 | 28-Oct-14 | 30-Oct-14 | 35 |
| L1BOH2-8116 | Finish Carpentry / Millwork | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 20 |
| L1BOH2-8126 | Doors & Hardware | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 22 |
| CO-7100T | CO - Preliminary Start-Up & Testing (Tower) | 10 | 10 | 29-Oct-14 | 12-Nov-14 | 10 |
| L17-8121 | Install Bathroom "Barn Doors" | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 22 |
| L03-8206a | Install Base @ Corridors | 3 | 3 | 29-Oct-14 | 31-Oct-14 | 24 |
| L03-8646 | Pool - Health inspections | 1 | 1 | 30-Oct-14 | 30-Oct-14 | 38 |
| LL1-Z2-8118a | Install decorative light fixtures | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 24 |
| L03-8614 | L3 Pool - Paint/wall finishes | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 14 |
| L03-8618 | L3 Pool - Ceramic tile | 5 | 5 | 31-Oct-14 | 06-Nov-14 | 12 |
| L11-8206a | Install Base @ Corridors | 3 | 3 | 01-Nov-14 | 04-Nov-14 | 31 |
| L1BOH2-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 22 |
| L1BOH2-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 22 |
| L1BOH2-8204 | Mech Trim / Finish (HVAC & Plumbing) | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 20 |
| L16-8129 | Install Shower Doors | 4 | 4 | 03-Nov-14 | 06-Nov-14 | 16 |
| L15-8138 | Install Toilet Accessories | 4 | 4 | 03-Nov-14 | 06-Nov-14 | 10 |
| LL1-8124a | Install Base | 4 | 4 | 03-Nov-14 | 06-Nov-14 | 17 |
| L1K-8124b | Install Base | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 19 |
| L1BOH2-8201 | Final Coat Finish Paint | 5 | 5 | 05-Nov-14 | 12-Nov-14 | 22 |
| L16-8138 | Install Toilet Accessories | 4 | 4 | 06-Nov-14 | 12-Nov-14 | 10 |
| L03-8620 | L3 Pool - Plumbing Fixtures & Trim / Finish | 5 | 5 | 07-Nov-14 | 14-Nov-14 | 12 |
| L03-8622 | L3 Pool - HVAC trim / Finish | 5 | 5 | 07-Nov-14 | 14-Nov-14 | 12 |
| L03-8624 | L3 Pool - Fire Sprinkler Trim / Finish | 5 | 5 | 07-Nov-14 | 14-Nov-14 | 12 |

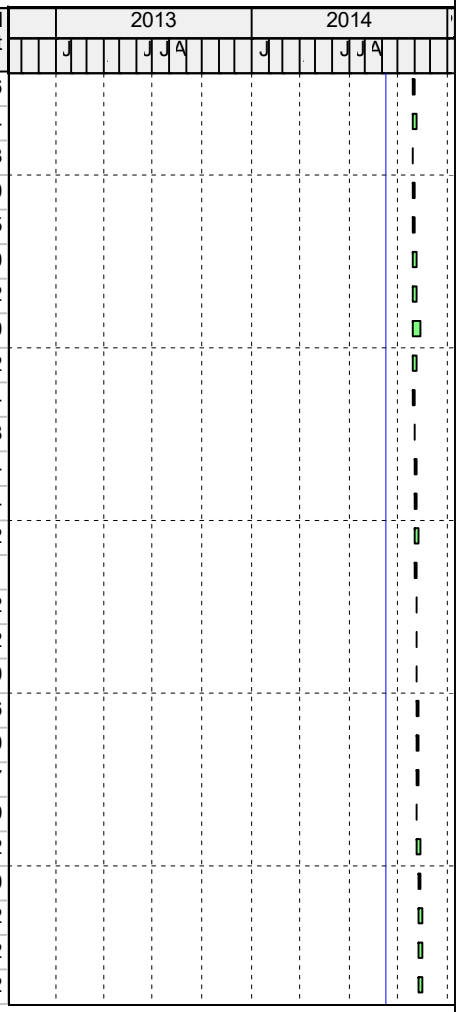



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8626 | L3 Pool - Elec Trim/ Finish | 5 | 5 | 07-Nov-14 | 14-Nov-14 | 12 |
| L03-8628 | L3 Pool - Elec Specialties Trim / Finish | 5 | 5 | 07-Nov-14 | 14-Nov-14 | 12 |
| L17-8129 | Install Shower Doors | 4 | 4 | 07-Nov-14 | 13-Nov-14 | 16 |
| L12-8206a | Install Base @ Corridors | 3 | 3 | 07-Nov-14 | 10-Nov-14 | 26 |
| L14-8206a | Install Base @ Corridors | 3 | 3 | 10-Nov-14 | 12-Nov-14 | 24 |
| LL1-Z3-8340 | Install walk-in cooler/freezer (BY OTHERS) | 5 | 5 | 11-Nov-14* | 17-Nov-14 | 17 |
| L17-8138 | Install Toilet Accessories | 4 | 4 | 11-Nov-14 | 14-Nov-14 | 10 |
| L1BOH2-8134 | Clean | 4 | 4 | 13-Nov-14 | 18-Nov-14 | 22 |
| L1BOH2-8132 | Punch | 4 | 4 | 13-Nov-14 | 18-Nov-14 | 22 |
| CO-7102T | CO - HVAC Commissioning (Tower) | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 25 |
| CO-7110T | Fire Sprinkler Pre-Testing (Tower) | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 20 |
| CO-7116T | Fire Alarm Pre-Testing (Tower) | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 20 |
| CO-7104T | Smoke Control Pre-Testing (Tower) | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 20 |
| L03-8630 | L3 Pool - Doors & Hardware | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 12 |
| L15-8206a | Install Base @ Corridors | 3 | 3 | 17-Nov-14 | 19-Nov-14 | 18 |
| LL1-Z3-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 18-Nov-14* | 19-Nov-14 | 17 |
| L1BOH2-8210 | Owner Walk / Create Punchlist | 1 | 1 | 19-Nov-14 | 19-Nov-14 | 22 |
| L1BOH2-8212 | Resolve Final Punchlist | 3 | 3 | 20-Nov-14 | 24-Nov-14 | 22 |
| I-3102 | Ballroom ceilings - additional work per ASIs 18, 25 | 4 | 4 | 20-Nov-14 | 25-Nov-14 | 6 |
| L1B-8120 | Install operable partitions | 3 | 3 | 20-Nov-14 | 24-Nov-14 | 7 |
| CO-7112T | City of Bellevue Fire Sprinkler Inspection / Approval (T | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 20 |
| CO-7118T | City of Bellevue Fire Alarm Inspection / Approval (Tow | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 20 |
| CO-7106T | City of Bellevue Smoke Control Testing (Tower) | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 20 |
| L1B-8128 | Install Base | 2 | 2 | 20-Nov-14 | 21-Nov-14 | 8 |
| L16-8206a | Install Base @ Corridors | 3 | 3 | 20-Nov-14 | 22-Nov-14 | 12 |
| I-1602 | Enclosure at manlift - Framing & windows | 6 | 6 | 24-Nov-14 | 03-Dec-14 | 12 |
| L1K-8128 | Install Kitchen equipment (BY OTHERS) | 10 | 10 | 24-Nov-14 | 09-Dec-14 | 13 |

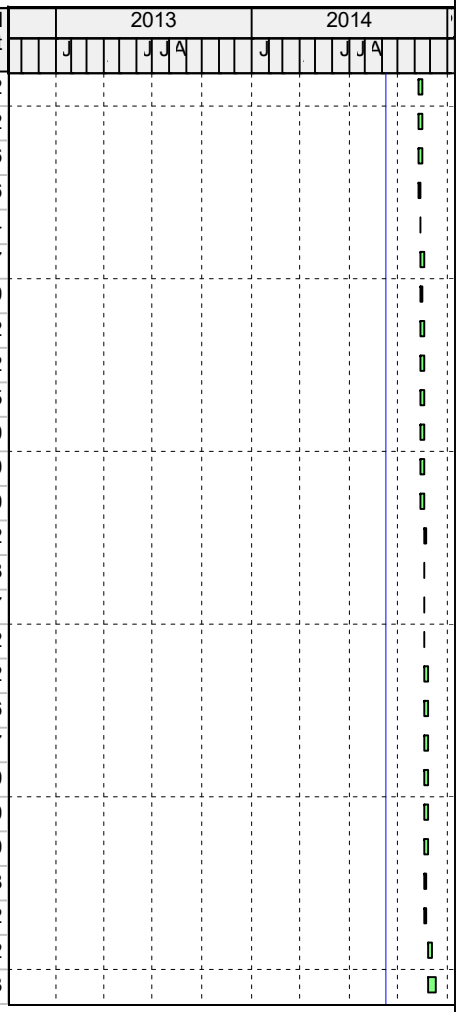



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8632 | L3 Pool - Install Bathroom Accessories | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 12 |
| L17-8206a | Install Base @ Corridors | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 12 |
| L1BOH2-81214 | L1, Zone 3 Complete | 0 | 0 | | 24-Nov-14 | 22 |
| I-1604 | Enclosure at manlift - GWB | 6 | 6 | 01-Dec-14 | 08-Dec-14 | 12 |
| L1L-8124a | Install Base | 3 | 3 | 02-Dec-14 | 04-Dec-14 | 2 |
| CM-1024 | Tower - "Clean/Punch" Complete - All Floors | 0 | 0 | | 02-Dec-14 | 23 |
| I-1202 | Concierge Lounge - Additional flooring work | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 0 |
| I-1204 | Concierge Lounge - Additional millwork | 4 | 4 | 03-Dec-14 | 08-Dec-14 | 0 |
| I-1606 | Enclosure at manlift - Paint & finishes | 4 | 4 | 03-Dec-14 | 08-Dec-14 | 12 |
| I-1608 | Enclosure at manlift - Metal panels (Elev 32) | 6 | 6 | 03-Dec-14 | 10-Dec-14 | 12 |
| L1L-8120 | Install plumbing at bar | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 2 |
| L1L-8122 | Install electrical at bar | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 2 |
| CM-1022 | Podium - "Clean/Punch" Complete - All Floors, All Zon | 0 | 0 | | 19-Dec-14 | 10 |
| CO-7124 | Complete Final Building Inspections | 5 | 5 | 31-Dec-14 | 07-Jan-15 | 0 |
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13 A | | |
| CM-1002 | CM - Contract Time (578 Cal Days) | 576 | 28 | 06-Mar-13 A | 05-Oct-14 | 94 |
| CM-1014 | CM - Start of Construction | 0 | 0 | 05-Apr-13 A | | |
| CM-1006 | Construction Documents Issued by Client - (Due on 7 | 0 | 0 | 08-Sep-14 | | 122 |
| CM-1008 | Finalization of Allowances - (Due on 9-2-13) | 0 | 0 | 08-Sep-14 | | 122 |
| CO-7004 | CO - Prep / Submit O&M Manuals | 40 | 40 | 05-Oct-14 | 13-Nov-14 | 55 |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 13-Nov-14 | | 14 |
| CM-1016 | CM - Owner FF+E "Build-Out" | 42 | 42 | 13-Nov-14 | 24-Dec-14 | 14 |
| CM-1018 | CM - Hotel Operations Training | 21 | 21 | 28-Nov-14* | 18-Dec-14 | 20 |
| CO-7006 | CO - Certificate of Occupancy/Substantial Completior | 0 | 0 | | 07-Jan-15 | 0 |

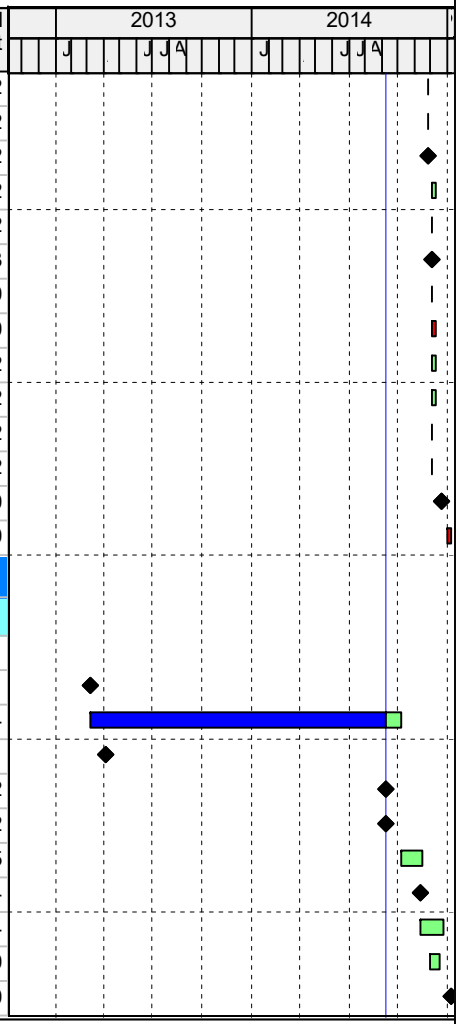


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7122 | CO - Certificate of Occupancy | 0 | 0 | | 07-Jan-15 | 0 |
| **Misc Milestones** | | | | | | |
| CM-1020 | MM - Site Mobilization | 10 | 0 | 06-Mar-13 A | 04-Apr-13 A | |
| MM-1008 | MM - Top Out - Tower / Structure | 0 | 0 | | 16-Apr-14 A | |
| MM-1004 | MM - Start Drywall In Tower | 0 | 0 | 27-Jun-14 A | | |
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 06-Sep-14 A | |
| MM-1010 | Energize Permanent Power | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 65 |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| Tower Crane | | | | | | |
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 0 | 04-Jun-13 A | 14-Jun-13 A | |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 0 | 20-Jun-13 A | 24-Jun-13 A | |
| TC-5902 | Tower Crane - Erectiion | 2 | 0 | 21-Jun-13 A | 24-Jun-13 A | |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 24-Jun-13 A | | |
| TC-5906 | Tower Crane - Operatational Period | 391 | 0 | 24-Jun-13 A | 16-Jun-14 A | |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 0 | 16-Jun-14 A | 17-Jun-14 A | |
| Man & Material Lifts | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 0 | 14-Jan-14 A | 20-Jan-14 A | |
| ML-5952 | Man/Material Lifts - Erect/Build Loading Dock | 5 | 0 | 21-Jan-14 A | 27-Jan-14 A | |
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 10-Feb-14 A | | |
| ML-5954 | Man/Material Lifts - Load Test / Certify | 1 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| ML-5958 | Man/Material Lifts - Operatational Period | 196 | 70 | 10-Feb-14 A | 16-Nov-14 | 18 |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 12 |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |
| Mass Excavation / Shoring | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 0 | 05-Apr-13 A | 12-Apr-13 A | |

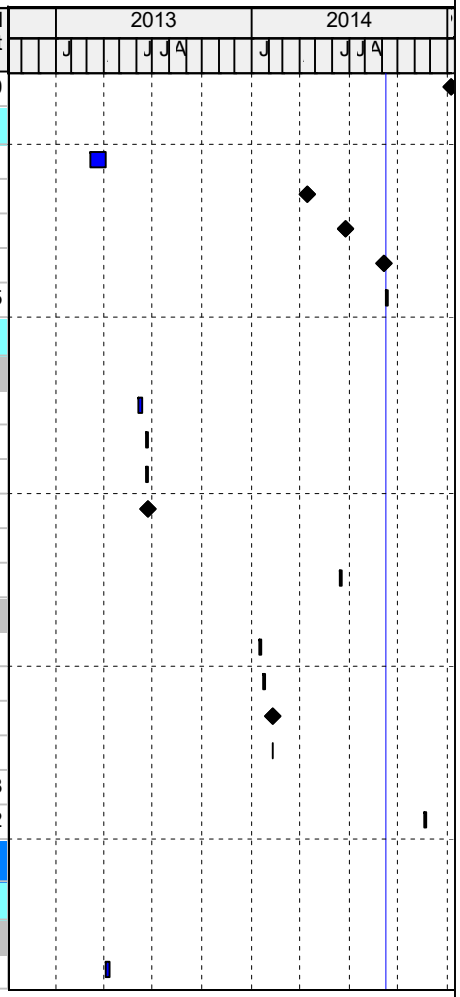



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2002 | Demolition And Utility Relocation | 8 | 0 | 15-Apr-13 A | 19-Apr-13 A | |
| SW-2010 | Grade Subgrade for Elect/Plumbing | 3 | 0 | 07-Jan-14 A | 09-Jan-14 A | |
| **Site Finishes** | | | | | | |
| SW-2006 | Install Perm Power Electrical Service / Dry Utilities (Offl | 15 | 0 | 20-May-14 A | 05-Jun-14 A | |
| SW-2004 | Offsite Water & Water Connection | 7 | 7 | 08-Sep-14 | 16-Sep-14 | 50 |
| SW-2008 | Sidewalks / Landscaping / Street Improvements | 20 | 20 | 23-Oct-14 | 25-Nov-14 | 17 |
| **Structure** | | | | | | |
| **Foundation / Substructure - (Levels LL4 / LL3)** | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 0 | 12-Jun-13 A | 27-Jun-13 A | |
| LL4-1601 | LL4 - Excavate Footings | 14 | 0 | 17-Jun-13 A | 30-Jul-13 A | |
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 0 | 18-Jun-13 A | 24-Jun-13 A | |
| LL4-1606 | LL4 - Undrgmd Plumbing | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-1608 | LL4 - Undrgmd Elec | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 0 | 19-Jun-13 A | 25-Jun-13 A | |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 0 | 26-Jun-13 A | 02-Aug-13 A | |
| LL4-2033 | LL4 - Shotcrete Walls | 27 | 0 | 26-Jun-13 A | 05-Aug-13 A | |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 0 | 03-Jul-13 A | 21-Aug-13 A | |
| LL4-1614 | LL4 - FRP SOG | 5 | 0 | 10-Jul-13 A | 07-Aug-13 A | |
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 0 | 12-Jul-13 A | 26-Jul-13 A | |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 0 | 13-Jul-13 A | 06-Aug-13 A | |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 0 | 22-Jul-13 A | 24-Jul-13 A | |
| LL4-1618 | LL4 - FRP Ramp SOG | 5 | 0 | 01-Aug-13 A | 07-Aug-13 A | |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2004 | LL2 - Shore / Form Deck | 8 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2006 | LL3 - M & E Inserts | 4 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2008 | LL3 - ReSteel / PT Cables | 6 | 0 | 05-Aug-13 A | 09-Aug-13 A | |

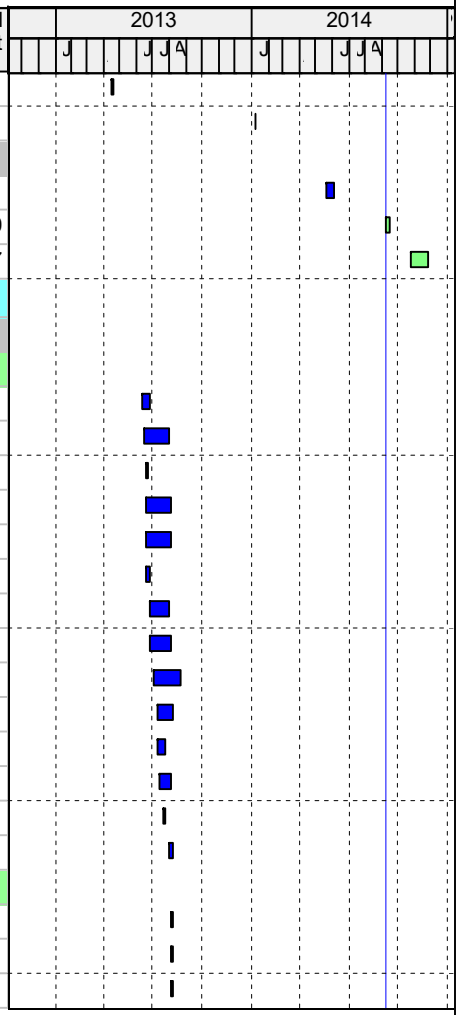


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-2010 | LL3 - Install Embeds | 2 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2001 | LL3 - Waterproof Walls | 3 | 0 | 05-Aug-13 A | 05-Aug-13 A | |
| LL3-2012 | LL3 - Pour / Finish Deck | 2 | 0 | 16-Aug-13 A | 16-Aug-13 A | |
| LL3-2014 | LL3 - Stress Tendons | 1 | 0 | 19-Aug-13 A | 19-Aug-13 A | |
| LL3-2000 | LL3 - FRP Core Walls | 8 | 0 | 19-Aug-13 A | 28-Aug-13 A | |
| LL3-2033 | LL3 - Shotcrete Walls | 5 | 0 | 23-Aug-13 A | 26-Aug-13 A | |
| LL3-2016 | LL3 - Strip / ReShore Deck | 3 | 0 | 01-Sep-13 A | 13-Sep-13 A | |
| LL3-2018 | LL3 - Remove ReShores | 4 | 0 | 04-Nov-13 A | 07-Nov-13 A | |
| Lower Podium - (Levels LL2 / LL1 / 1 / 2) | | | | | | |
| Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock) | | | | | | |
| Grids 1 to 4 - (SOG @ Loading Dock) | | | | | | |
| LL2-2056 | LL2 - Grease Intercepter | 5 | 0 | 15-Aug-13 A | 21-Aug-13 A | |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 0 | 27-Aug-13 A | 04-Sep-13 A | |
| LL2-2027 | LL2 - Waterproof Walls | 2 | 0 | 27-Aug-13 A | 28-Aug-13 A | |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 0 | 30-Aug-13 A | 05-Sep-13 A | |
| LL2-2021 | LL2 - FRP Elec Vault | 14 | 0 | 30-Aug-13 A | 04-Sep-13 A | |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 0 | 04-Sep-13 A | 11-Sep-13 A | |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 0 | 11-Sep-13 A | 13-Sep-13 A | |
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls/Roof | 11 | 0 | 19-Sep-13 A | 03-Oct-13 A | |
| LL2-2020 | LL2 - Undrgmd Plumbing | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2022 | LL2 - Undrgmd Elec | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2031 | LL2 - FRP Generator SOG | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2015 | LL2 to LL1 FRP Columns / Misc Walls | 6 | 0 | 01-Oct-13 A | 01-Oct-13 A | |
| LL2-2029 | LL2 - F/R/P Pour #2 | 8 | 0 | 15-Jan-14 A | 24-Jan-14 A | |
| LL2-2011 | LL2 - F/R/P Pour #3 | 16 | 0 | 24-Jan-14 A | 18-Feb-14 A | |
| LL2-2019 | LL2 - F/R/P Pour #6 | 4 | 0 | 19-Feb-14 A | 17-Mar-14 A | |

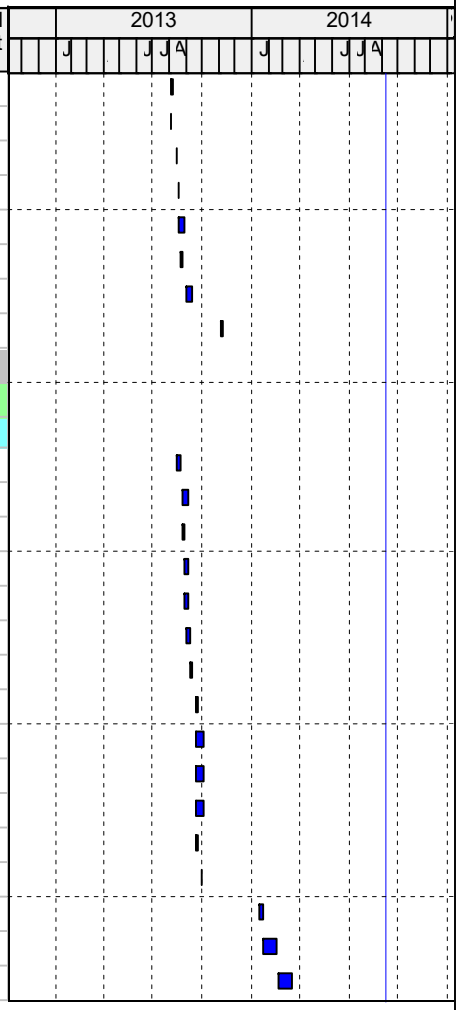



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2044 | LL2 - Set Generator | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |
| LL2-2004 | LL2 - Shore / Form Deck | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2035 | LL2 to LL1 - Shotcrete Walls | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2006 | LL2 - M & E Inserts | 4 | 0 | 14-Aug-13 A | 19-Aug-13 A | |
| LL2-2008 | LL2 - ReSteel / PT Cables | 6 | 0 | 14-Aug-13 A | 21-Aug-13 A | |
| LL2-2010 | LL2 - Install Embeds | 3 | 0 | 14-Aug-13 A | 16-Aug-13 A | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 0 | 27-Aug-13 A | 06-Sep-13 A | |
| LL2-2012 | LL2 - Place / Finish Deck | 3 | 0 | 29-Aug-13 A | 29-Aug-13 A | |
| LL2-2023 | LL2 - Waterproof Walls | 3 | 0 | 29-Aug-13 A | 03-Sep-13 A | |
| LL2-2014 | LL2 - Stress Tendons | 1 | 0 | 30-Aug-13 A | 30-Aug-13 A | |
| LL2-2016 | LL2 - Strip / ReShore | 3 | 0 | 03-Sep-13 A | 05-Sep-13 A | |
| LL2-8234 | LL2 - Place / Finish Deck | 3 | 0 | 12-Sep-13 A | 12-Sep-13 A | |
| LL2-2000 | LL2 - FRP Core Walls | 8 | 0 | 12-Sep-13 A | 23-Sep-13 A | |
| LL2-2018 | LL2 - Remove ReShores | 4 | 0 | 13-Nov-13 A | 18-Nov-13 A | |
| LL2-2013 | LL2 - F/R/P Pour #1 | 4 | 0 | 13-Jan-14 A | 16-Jan-14 A | |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| P5A-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2000 | LL1 - FRP Core Walls | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2004 | LL1 - Shore / Form Deck | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| P6-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P6-2004 | LL1 - Shore / Form Deck | 7 | 0 | 16-Sep-13 A | 24-Sep-13 A | |
| P5A-2006 | LL1 - MEP Rough In | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2008 | LL1 - ReSteel / PT Cables | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2012 | LL1 - Place / Finish Deck | 0 | 0 | 20-Sep-13 A | | |
| P5A-2020 | LL1 - Waterproof Walls | 3 | 0 | 20-Sep-13 A | 24-Sep-13 A | |

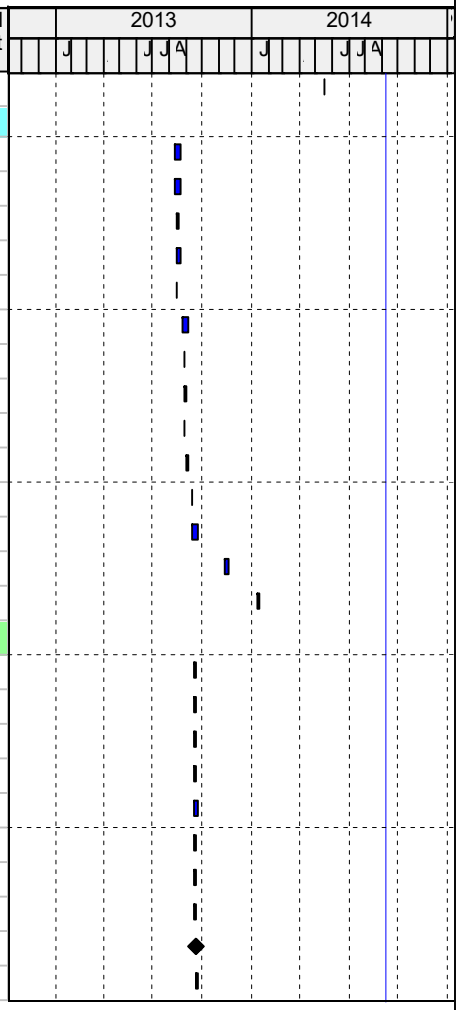



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P5A-2014 | LL1 - Stress Tendons | 1 | 0 | 23-Sep-13 A | 23-Sep-13 A | |
| P5A-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2006 | LL1 - MEP Rough In | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2008 | LL1 - ReSteel / PT Cables | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 24-Sep-13 A | 25-Sep-13 A | |
| P6-2020 | LL1 - Waterproof Walls | 4 | 0 | 24-Sep-13 A | 27-Sep-13 A | |
| P5A-2033 | LL1 - Resteel/Shotcrete Walls | 3 | 0 | 25-Sep-13 A | 27-Sep-13 A | |
| P5B-2002 | LL1 - FRP Columns Below | 5 | 0 | 26-Sep-13 A | 02-Oct-13 A | |
| P5B-2004 | LL1 - Shore / Form Deck | 7 | 0 | 26-Sep-13 A | 04-Oct-13 A | |
| P6-2012 | LL1 - Place / Finish Deck | 0 | 0 | 27-Sep-13 A | | |
| P6-2014 | LL1 - Stress Tendons | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2033 | LL1 - Resteel/Shotcrete Walls | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 01-Oct-13 A | 03-Oct-13 A | |
| P5B-2006 | LL1 - MEP Rough In | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2002 | FRP Columns Below | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2004 | Shore / Form Deck | 4 | 0 | 03-Oct-13 A | 08-Oct-13 A | |
| P5B-2008 | LL1 - ReSteel / PT Cables | 5 | 0 | 04-Oct-13 A | 10-Oct-13 A | |
| P5B-2010 | LL1 - Install Edgeform/Embeds | 4 | 0 | 04-Oct-13 A | 09-Oct-13 A | |
| P8-2002 | FRP Columns Below | 5 | 0 | 07-Oct-13 A | 11-Oct-13 A | |
| P8-2000 | Form/Resteel/Close Core Walls | 14 | 0 | 07-Oct-13 A | 24-Oct-13 A | |
| P8-2004 | Shore / Form Deck P8 | 8 | 0 | 07-Oct-13 A | 16-Oct-13 A | |
| P7-2002 | FRP Columns Below | 5 | 0 | 08-Oct-13 A | 14-Oct-13 A | |
| P7-2004 | Shore / Form Deck | 6 | 0 | 08-Oct-13 A | 15-Oct-13 A | |
| P10A--2006 | MEP Rough In | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2008 | ReSteel / PT Cables | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2010 | Install Edgeform/Embeds | 2 | 0 | 08-Oct-13 A | 09-Oct-13 A | |
| P5B-2012 | LL1 - Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |

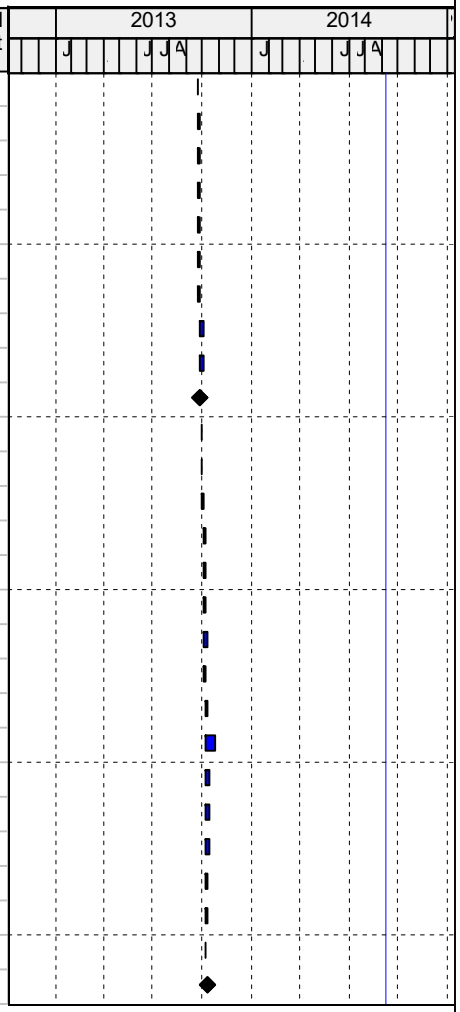



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P10A--2012 | Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P5B-2014 | LL1 - Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P7-2006 | MEP Rough In | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P7-2008 | ReSteel / PT Cables | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P10A--2014 | Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P8-2020 | Shore / Form Deck P9 | 6 | 0 | 14-Oct-13 A | 21-Oct-13 A | |
| P5B-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2010 | Install Edgeform/Embeds | 2 | 0 | 15-Oct-13 A | 16-Oct-13 A | |
| P8-2006 | MEP Rough In | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2008 | ReSteel / PT Cables | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2010 | Install Edgeform/Embeds | 4 | 0 | 15-Oct-13 A | 18-Oct-13 A | |
| P10A--2016 | Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2012 | Place / Finish Deck | 0 | 0 | 18-Oct-13 A | | |
| P7-2033 | Resteel/Shotcrete Walls | 3 | 0 | 18-Oct-13 A | 22-Oct-13 A | |
| P7-2014 | Stress Tendons | 1 | 0 | 21-Oct-13 A | 21-Oct-13 A | |
| P7-2016 | Strip / ReShore Deck | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2002 | FRP Columns Below | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P10B--2000 | FRP Shear Walls Below | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2004 | Shore / Form Deck | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P8-2012 | Place / Finish Deck P 8 & 9 and Core Walls | 0 | 0 | 25-Oct-13 A | | |
| P8-2014 | Stress Tendons | 1 | 0 | 28-Oct-13 A | 28-Oct-13 A | |
| P10B--2006 | MEP Rough In | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2008 | ReSteel / PT Cables | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2010 | Install Edgeform/Embeds | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P12--2002 | FRP Columns Below | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P12--2000 | Form/Resteel/Close Core Walls | 9 | 0 | 28-Oct-13 A | 07-Nov-13 A | |
| P12--2004 | Shore / Form Deck | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |

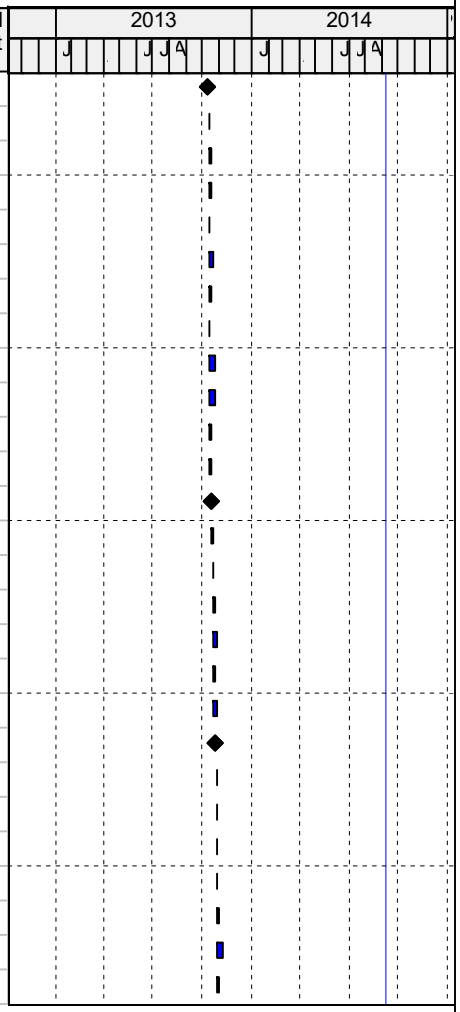



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P8-2016 | Strip / ReShore Deck | 3 | 0 | 29-Oct-13 A | 31-Oct-13 A | |
| P11–2002 | FRP Columns Below | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P11–2004 | Shore / Form Deck | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P10B–2012 | Place / Finish Deck | 0 | 0 | 31-Oct-13 A | | |
| P10B–2014 | Stress Tendons | 1 | 0 | 01-Nov-13 A | 01-Nov-13 A | |
| P12–2006 | MEP Rough In | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12–2008 | ReSteel / PT Cables | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12–2010 | Install Edgeform/Embeds | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P10B–2016 | Strip / ReShore Deck | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2006 | MEP Rough In | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2008 | ReSteel / PT Cables | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2010 | Install Edgeform/Embeds | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2012 | Place / Finish Deck | 0 | 0 | 07-Nov-13 A | | |
| P13–2002 | FRP Columns Below | 5 | 0 | 07-Nov-13 A | 14-Nov-13 A | |
| P13–2004 | Shore / Form Deck | 9 | 0 | 07-Nov-13 A | 28-Nov-13 A | |
| P11–2014 | Stress Tendons | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| P12–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 08-Nov-13 A | | |
| P11–2016 | Strip / ReShore Deck | 3 | 0 | 12-Nov-13 A | 14-Nov-13 A | |
| P12–2014 | Stress Tendons | 1 | 0 | 12-Nov-13 A | 12-Nov-13 A | |
| P14–2002 | FRP Columns Below | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P14–2000 | Form/Resteel/Close Core Walls | 8 | 0 | 19-Nov-13 A | 03-Dec-13 A | |
| P14–2004 | Shore / Form Deck | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P13A–2002 | FRP Columns Below | 5 | 0 | 21-Nov-13 A | 27-Nov-13 A | |
| P13A–2004 | Shore / Form Deck | 4 | 0 | 21-Nov-13 A | 26-Nov-13 A | |
| P13–2010 | Install Edgeform/Embeds | 5 | 0 | 22-Nov-13 A | 04-Dec-13 A | |
| P13–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2006 | MEP Rough In | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |

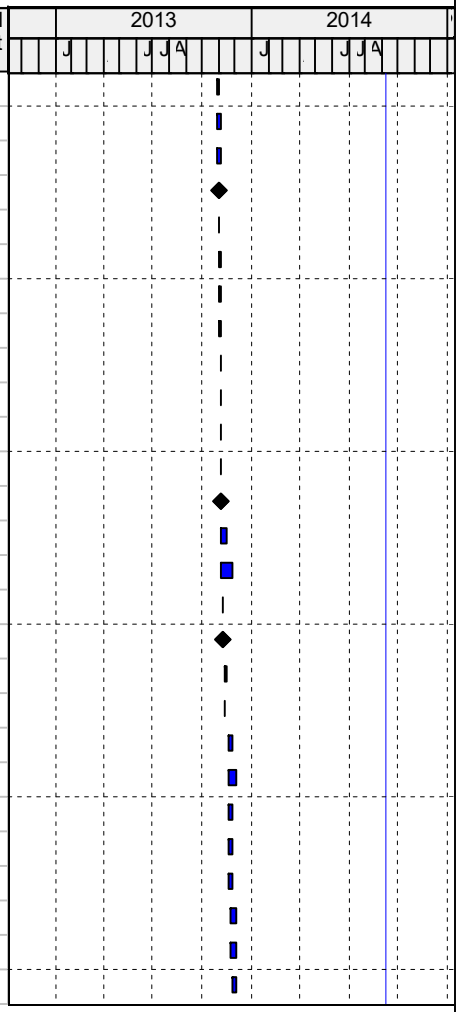



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P14–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2010 | Install Edgeform/Embeds | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P13–2006 | MEP Rough In | 5 | 0 | 26-Nov-13 A | 03-Dec-13 A | |
| P13A–2006 | MEP Rough In | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2008 | ReSteel / PT Cables | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2010 | Install Edgeform/Embeds | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13–2012 | Place / Finish Deck | 0 | 0 | 02-Dec-13 A | | |
| P13A–2012 | Place / Finish Deck | 0 | 0 | 03-Dec-13 A | | |
| P14–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 04-Dec-13 A | | |
| P13–2014 | Stress Tendons | 1 | 0 | 05-Dec-13 A | 05-Dec-13 A | |
| P15–2002 | FRP Columns Below | 3 | 0 | 05-Dec-13 A | 09-Dec-13 A | |
| P15–2000 | Jump/Resteel/Close Core | 9 | 0 | 05-Dec-13 A | 17-Dec-13 A | |
| P15–2004 | Shore / Form Deck | 5 | 0 | 05-Dec-13 A | 11-Dec-13 A | |
| P13–2016 | Strip / ReShore Deck | 3 | 0 | 06-Dec-13 A | 10-Dec-13 A | |
| P13A–2014 | Stress Tendons | 1 | 0 | 06-Dec-13 A | 06-Dec-13 A | |
| P14–2014 | Stress Tendons | 1 | 0 | 07-Dec-13 A | 07-Dec-13 A | |
| P15–2006 | MEP Rough In | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2008 | ReSteel / PT Cables | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2010 | Install Edgeform/Embeds | 3 | 0 | 11-Dec-13 A | 13-Dec-13 A | |
| P16-2002 | FRP Columns Below | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P16-2004 | Shore / Form Deck | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P15–2012 | Place / Finish Deck | 0 | 0 | 18-Dec-13 A | | |
| P15–2020 | Place Conc @ Core | 0 | 0 | 18-Dec-13 A | | |
| P16-2000 | Jump/Resteel/Close Core | 5 | 0 | 18-Dec-13 A | 24-Dec-13 A | |
| P16-2006 | MEP Rough In | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2008 | ReSteel / PT Cables | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2010 | Install Edgeform/Embeds | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |

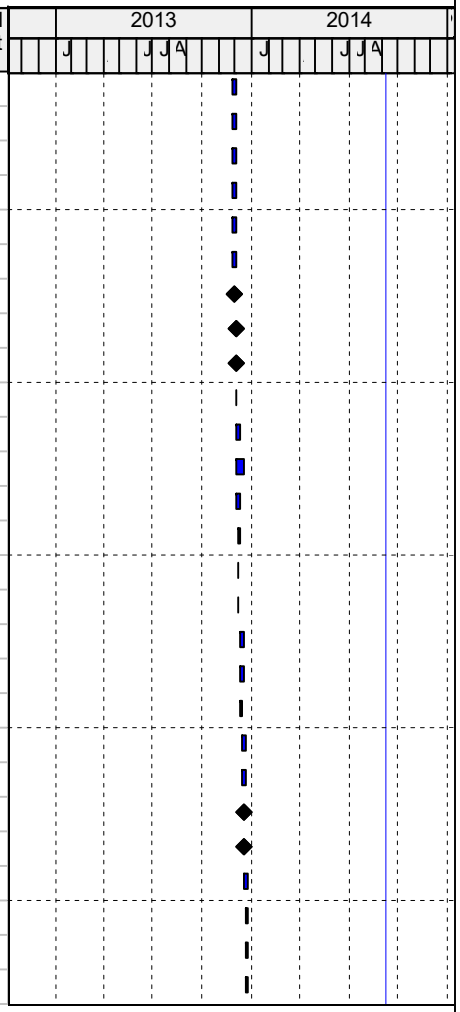



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P15–2014 | Stress Tendons | 1 | 0 | 21-Dec-13 A | 21-Dec-13 A | |
| P8-2018 | Remove Reshores | 2 | 0 | 23-Dec-13 A | 24-Dec-13 A | |
| P10A–2018 | Remove Reshores | 2 | 0 | 26-Dec-13 A | 27-Dec-13 A | |
| P16-2012 | Place / Finish Deck | 0 | 0 | 26-Dec-13 A | | |
| P16-2020 | Place Conc @ Core | 0 | 0 | 26-Dec-13 A | | |
| P17-2002 | FRP Columns Below | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P17-2000 | Jump/Resteel/Close Core | 7 | 0 | 27-Dec-13 A | 07-Jan-14 A | |
| P17-2004 | Shore / Form Deck | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P10B–2018 | Remove Reshores | 2 | 0 | 30-Dec-13 A | 31-Dec-13 A | |
| P16-2014 | Stress Tendons | 1 | 0 | 31-Dec-13 A | 31-Dec-13 A | |
| P5A-2018 | LL1 - Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P11–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P12–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P17-2006 | MEP Rough In | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2008 | ReSteel / PT Cables | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2010 | Install Edgeform/Embeds | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P6-2018 | LL1 - Remove Reshores | 2 | 0 | 06-Jan-14 A | 07-Jan-14 A | |
| P5B-2018 | LL1 - Remove Reshores | 2 | 0 | 08-Jan-14 A | 09-Jan-14 A | |
| P17-2012 | Place / Finish Deck | 0 | 0 | 08-Jan-14 A | | |
| P17-2020 | Place Conc @ Core | 0 | 0 | 08-Jan-14 A | | |
| P18-2002 | FRP Columns Below | 5 | 0 | 09-Jan-14 A | 15-Jan-14 A | |
| P18-2000 | Jump/Resteel/Close Core | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P18-2004 | Shore / Form Deck | 3 | 0 | 09-Jan-14 A | 13-Jan-14 A | |
| LL2-2022R | MEP Rough In | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P7-2018 | Remove Reshores | 2 | 0 | 10-Jan-14 A | 13-Jan-14 A | |
| P17-2014 | Stress Tendons | 1 | 0 | 11-Jan-14 A | 11-Jan-14 A | |
| P13–2018 | Remove Reshores | 2 | 0 | 13-Jan-14 A | 14-Jan-14 A | |

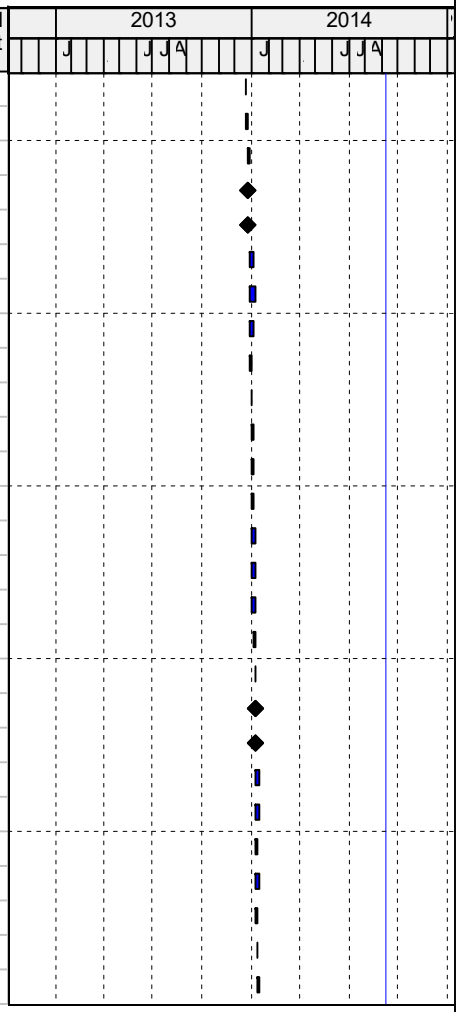



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P13A--2018 | Remove Reshores | 2 | 0 | 15-Jan-14 A | 16-Jan-14 A | |
| WEA-2012 | WIND IMPACT | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| P18-2006 | MEP Rough In | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2008 | ReSteel / PT Cables | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2010 | Install Edgeform/Embeds | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2012 | Place / Finish Deck | 0 | 0 | 22-Jan-14 A | | |
| P18-2020 | Place Conc @ Core | 0 | 0 | 22-Jan-14 A | | |
| P19-2002 | FRP Columns Below | 5 | 0 | 23-Jan-14 A | 29-Jan-14 A | |
| P19-2000 | Jump/Resteel/Close Core | 4 | 0 | 23-Jan-14 A | 28-Jan-14 A | |
| P19-2004 | Shore / Form Deck | 3 | 0 | 23-Jan-14 A | 27-Jan-14 A | |
| P18-2014 | Stress Tendons | 1 | 0 | 25-Jan-14 A | 25-Jan-14 A | |
| P14--2018 | Remove Reshores | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2006 | MEP Rough In | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2008 | ReSteel / PT Cables | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2010 | Install Edgeform/Embeds | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2012 | Place / Finish Deck | 0 | 0 | 29-Jan-14 A | | |
| P19-2020 | Place Conc @ Core | 0 | 0 | 29-Jan-14 A | | |
| P20-2002 | FRP Columns Below | 5 | 0 | 30-Jan-14 A | 05-Feb-14 A | |
| P20-2000 | Jump/Resteel/Close Core | 9 | 0 | 30-Jan-14 A | 11-Feb-14 A | |
| P20-2004 | Shore / Form Deck | 6 | 0 | 30-Jan-14 A | 10-Feb-14 A | |
| P19-2014 | Stress Tendons | 1 | 0 | 01-Feb-14 A | 01-Feb-14 A | |
| P13A--2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P14--2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P15--2016 | Strip / ReShore Deck | 3 | 0 | 06-Feb-14 A | 10-Feb-14 A | |
| P20-2006 | MEP Rough In | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2008 | ReSteel / PT Cables | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2010 | Install Edgeform/Embeds | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |

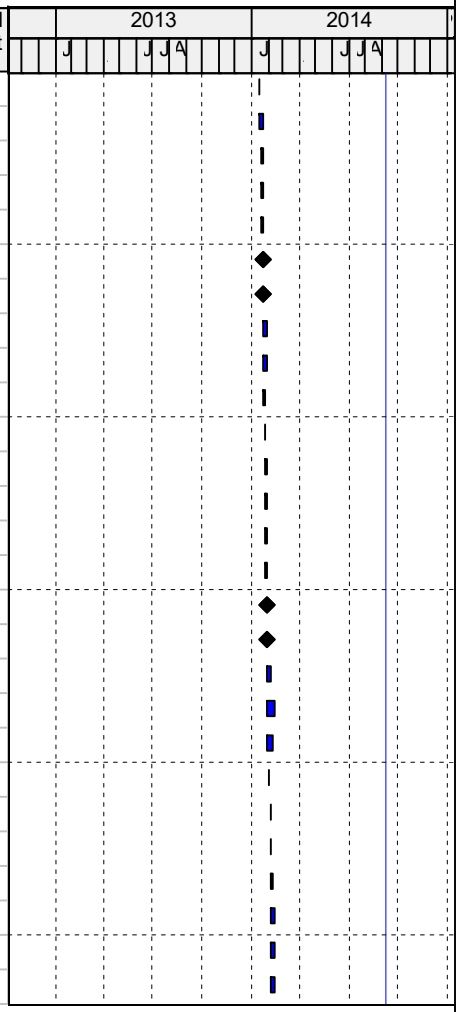


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 06-Feb-14 A | 12-Feb-14 A | |
| P16-2016 | Strip / ReShore Deck | 3 | 0 | 10-Feb-14 A | 12-Feb-14 A | |
| L04-2018 | Remove Reshores | 2 | 0 | 10-Feb-14 A | 11-Feb-14 A | |
| L03-2018 | Remove Reshores | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| P17-2016 | Strip / ReShore Deck | 3 | 0 | 12-Feb-14 A | 14-Feb-14 A | |
| P20-2012 | Place / Finish Deck | 0 | 0 | 12-Feb-14 A | | |
| P20-2020 | Place Conc @ Core | 0 | 0 | 12-Feb-14 A | | |
| L04-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-Feb-14 A | 18-Feb-14 A | |
| P12–2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P18-2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P21-2002 | FRP Columns Below | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| P21-2000 | Jump/Resteel/Close Core | 4 | 0 | 13-Feb-14 A | 18-Feb-14 A | |
| P21-2004 | Shore / Form Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P19-2016 | Strip / ReShore Deck | 3 | 0 | 14-Feb-14 A | 18-Feb-14 A | |
| P20-2014 | Stress Tendons | 1 | 0 | 15-Feb-14 A | 15-Feb-14 A | |
| P21-2006 | MEP Rough In | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2008 | ReSteel / PT Cables | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P20-2016 | Strip / ReShore Deck | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| L05-2018 | Remove Reshores | 2 | 0 | 18-Feb-14 A | 19-Feb-14 A | |
| P21-2012 | Place / Finish Deck | 0 | 0 | 19-Feb-14 A | | |
| P21-2020 | Place Conc @ Core | 0 | 0 | 19-Feb-14 A | | |
| P22-2002 | FRP Columns Below | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P22-2000 | Jump/Resteel/Close Core | 4 | 0 | 20-Feb-14 A | 25-Feb-14 A | |
| P22-2004 | Shore / Form Deck | 3 | 0 | 20-Feb-14 A | 24-Feb-14 A | |
| L05-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P21-2014 | Stress Tendons | 1 | 0 | 22-Feb-14 A | 22-Feb-14 A | |

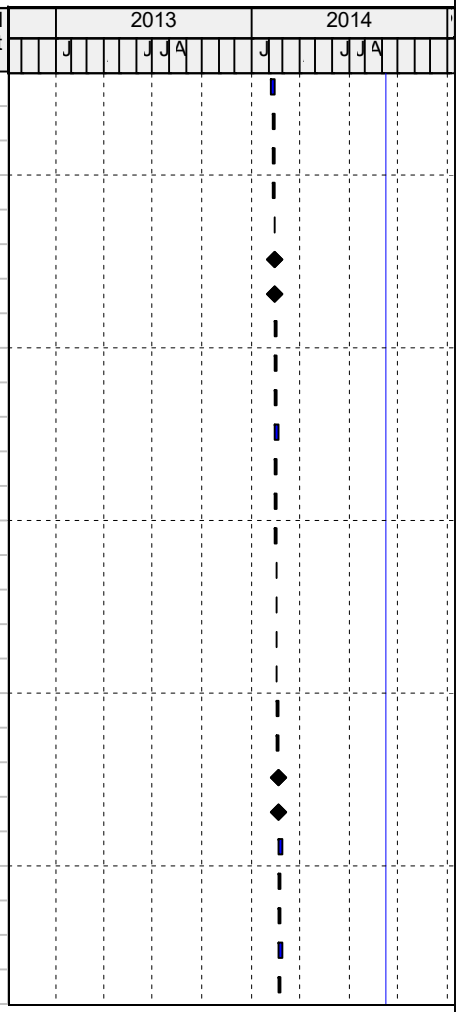



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P21-2016 | Strip / ReShore Deck | 3 | 0 | 24-Feb-14 A | 26-Feb-14 A | |
| P22-2006 | MEP Rough In | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2008 | ReSteel / PT Cables | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| L06-2018 | Remove Reshores | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| P22-2012 | Place / Finish Deck | 0 | 0 | 26-Feb-14 A | | |
| P22-2020 | Place Conc @ Core | 0 | 0 | 26-Feb-14 A | | |
| P23-2002 | FRP Columns Below | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2000 | Jump/Resteel/Close Core | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2004 | Shore / Form Deck | 3 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2006 | MEP Rough In | 2 | 0 | 01-Mar-14 A | 03-Mar-14 A | |
| P22-2014 | Stress Tendons | 1 | 0 | 01-Mar-14 A | 01-Mar-14 A | |
| P23-2008 | ReSteel / PT Cables | 2 | 0 | 03-Mar-14 A | 04-Mar-14 A | |
| P22-2016 | Strip / ReShore Deck | 3 | 0 | 04-Mar-14 A | 10-Mar-14 A | |
| P23-2010 | Install Edgeform/Embeds | 2 | 0 | 04-Mar-14 A | 04-Mar-14 A | |
| L07-2018 | Remove Reshores | 2 | 0 | 04-Mar-14 A | 05-Mar-14 A | |
| P23-2012 | Place / Finish Deck | 0 | 0 | 05-Mar-14 A | | |
| P23-2020 | Place Conc @ Core | 0 | 0 | 05-Mar-14 A | | |
| P24-2002 | FRP Columns Below | 5 | 0 | 05-Mar-14 A | 07-Mar-14 A | |
| P24-2004 | Shore / Form Deck | 3 | 0 | 06-Mar-14 A | 10-Mar-14 A | |
| P24-2000 | Jump/Resteel/Close Core | 4 | 0 | 08-Mar-14 A | 10-Mar-14 A | |
| P23-2014 | Stress Tendons | 1 | 0 | 10-Mar-14 A | 10-Mar-14 A | |
| P24-2008 | ReSteel / PT Cables | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P24-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P23-2016 | Strip / ReShore Deck | 3 | 0 | 11-Mar-14 A | 17-Mar-14 A | |
| P24-2006 | MEP Rough In | 2 | 0 | 11-Mar-14 A | 11-Mar-14 A | |
| P25-2002 | FRP Columns Below | 5 | 0 | 11-Mar-14 A | 13-Mar-14 A | |

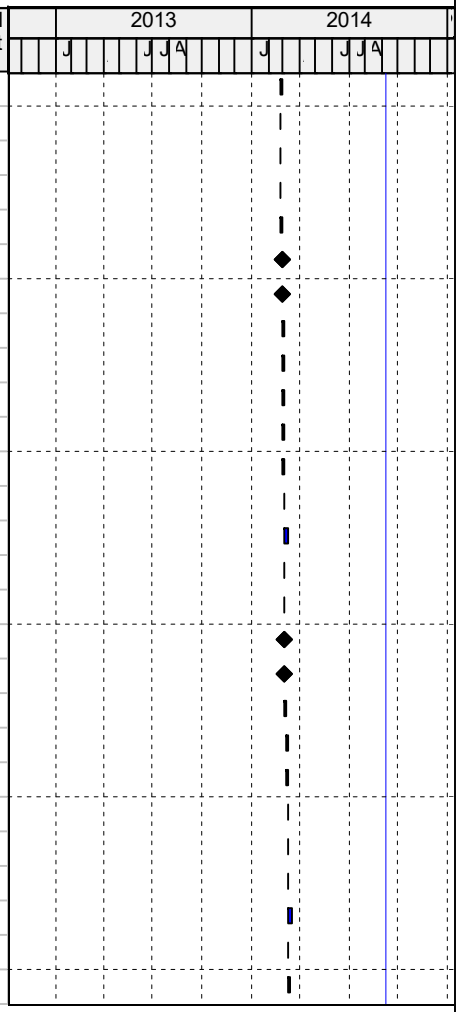



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-2018 | Remove Reshores | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| P24-2012 | Place / Finish Deck | 0 | 0 | 12-Mar-14 A | | |
| P24-2020 | Place Conc @ Core | 0 | 0 | 12-Mar-14 A | | |
| P25-2004 | Shore / Form Deck | 3 | 0 | 13-Mar-14 A | 17-Mar-14 A | |
| P25-2000 | Jump/Resteel/Close Core | 4 | 0 | 15-Mar-14 A | 17-Mar-14 A | |
| P24-2014 | Stress Tendons | 1 | 0 | 17-Mar-14 A | 17-Mar-14 A | |
| P25-2006 | MEP Rough In | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2008 | ReSteel / PT Cables | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| L06-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 18-Mar-14 A | 20-Mar-14 A | |
| L09-2018 | Remove Reshores | 2 | 0 | 18-Mar-14 A | 19-Mar-14 A | |
| P26-2002 | FRP Columns Below | 5 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| P25-2012 | Place / Finish Deck | 0 | 0 | 19-Mar-14 A | | |
| P25-2020 | Place Conc @ Core | 0 | 0 | 19-Mar-14 A | | |
| P26-2004 | Shore / Form Deck | 3 | 0 | 20-Mar-14 A | 24-Mar-14 A | |
| L07-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 21-Mar-14 A | 25-Mar-14 A | |
| P26-2000 | Jump/Resteel/Close Core | 4 | 0 | 22-Mar-14 A | 24-Mar-14 A | |
| P26-2006 | MEP Rough In | 2 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P26-2008 | ReSteel / PT Cables | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P26-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P25-2014 | Stress Tendons | 1 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P27-2002 | FRP Columns Below | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| P26-2012 | Place / Finish Deck | 0 | 0 | 26-Mar-14 A | | |
| P26-2020 | Place Conc @ Core | 0 | 0 | 26-Mar-14 A | | |
| L08-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 26-Mar-14 A | 28-Mar-14 A | |
| L10-2018 | Remove Reshores | 2 | 0 | 26-Mar-14 A | 27-Mar-14 A | |
| P27-2004 | Shore / Form Deck | 3 | 0 | 27-Mar-14 A | 31-Mar-14 A | |

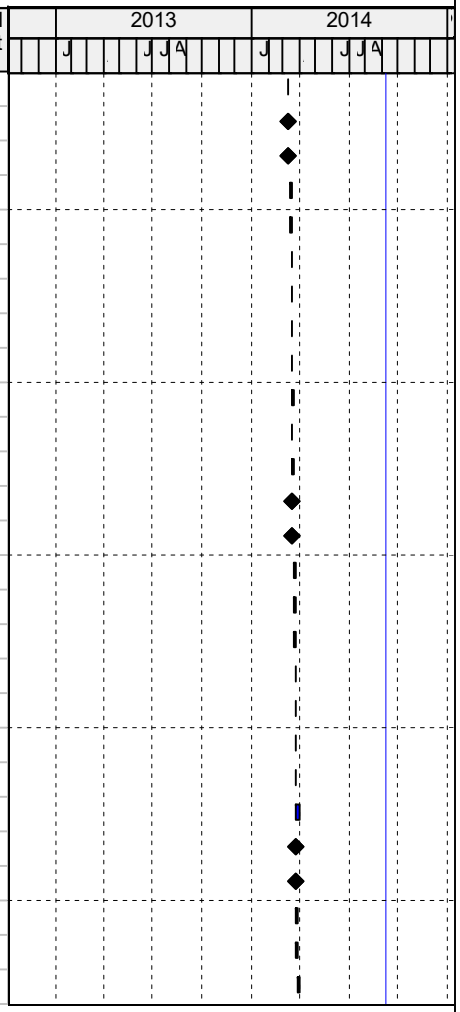



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P27-2000 | Jump/Resteel/Close Core | 4 | 0 | 29-Mar-14 A | 31-Mar-14 A | |
| P27-2006 | MEP Rough In | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2008 | ReSteel / PT Cables | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2010 | Install Edgeform/Embeds | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P26-2014 | Stress Tendons | 1 | 0 | 31-Mar-14 A | 31-Mar-14 A | |
| L09-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 31-Mar-14 A | 02-Apr-14 A | |
| P24-2016 | Strip / ReShore Deck | 3 | 0 | 01-Apr-14 A | 07-Apr-14 A | |
| L11-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 02-Apr-14 A | |
| L12-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 03-Apr-14 A | |
| P27-2012 | Place / Finish Deck | 0 | 0 | 02-Apr-14 A | | |
| P27-2020 | Place Conc @ Core | 0 | 0 | 02-Apr-14 A | | |
| P28-2002 | FRP Columns Below | 5 | 0 | 02-Apr-14 A | 04-Apr-14 A | |
| P28-2004 | Shore / Form Deck | 4 | 0 | 03-Apr-14 A | 08-Apr-14 A | |
| L10-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| P27-2014 | Stress Tendons | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| P25-2016 | Strip / ReShore Deck | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L14-2018 | Remove Reshores | 2 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| P28-2000 | Jump/Resteel/Close Core | 7 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| P28-2006 | MEP Rough In | 4 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2008 | ReSteel / PT Cables | 4 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Apr-14 A | 11-Apr-14 A | |
| L12-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| P28-2012 | Place / Finish Deck | 0 | 0 | 14-Apr-14 A | | |
| P28-2020 | Place Conc @ Core | 0 | 0 | 14-Apr-14 A | | |
| P29-2002 | FRP Columns Above Roof Deck | 3 | 0 | 14-Apr-14 A | 18-Apr-14 A | |
| P26-2016 | Strip / ReShore Deck | 3 | 0 | 14-Apr-14 A | 17-Apr-14 A | |

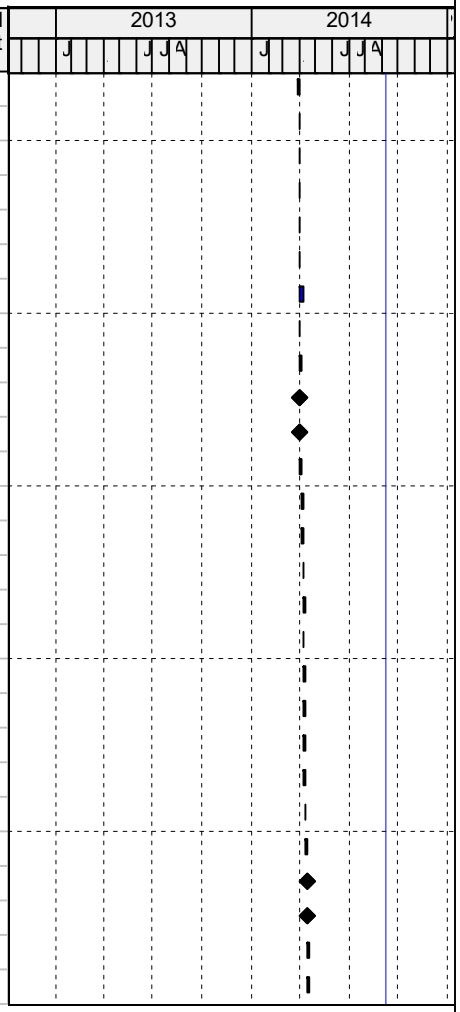



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-Apr-14 A | 18-Apr-14 A | |
| P28-2014 | Stress Tendons | 1 | 0 | 17-Apr-14 A | 17-Apr-14 A | |
| P29-2000 | Strip Core | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| P27-2016 | Strip / ReShore Deck | 3 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L15-2018 | Remove Reshores | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| P28-2016 | Strip / ReShore Deck | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L15-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L16-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-May-14 A | 19-May-14 A | |
| L16-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2019 | Grind Ceiling for Skim Coat | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| **Ballroom Catwalk & Roof** | | | | | | |
| PC-2100 | Erect Structural Steel @ Porte Cochere | 3 | 0 | 30-Jan-14 A | 03-Feb-14 A | |
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 7 | 0 | 07-Feb-14 A | 17-Feb-14 A | |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| PC-2102 | Metal Decking @ Porte Cochere/ Roof | 2 | 0 | 17-Apr-14 A | 18-Apr-14 A | |
| BR-2112 | BR - Fireproofing @ Structural Steel | 2 | 0 | 27-May-14 A | 30-May-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Mech Penthouse** | | | | | | |
| PH-8706 | Set Mech Equipment @ Tower Roof | 3 | 0 | 22-May-14 A | 28-May-14 A | |
| PH-8708 | Set Equipment @ Penthouse | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| PH-8700 | PH - Structural Steel and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| **Vertical Circulation** | | | | | | |
| **Stairs** | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 25-Nov-13 A | 26-Nov-13 A | |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 27-Nov-13 A | 03-Dec-13 A | |

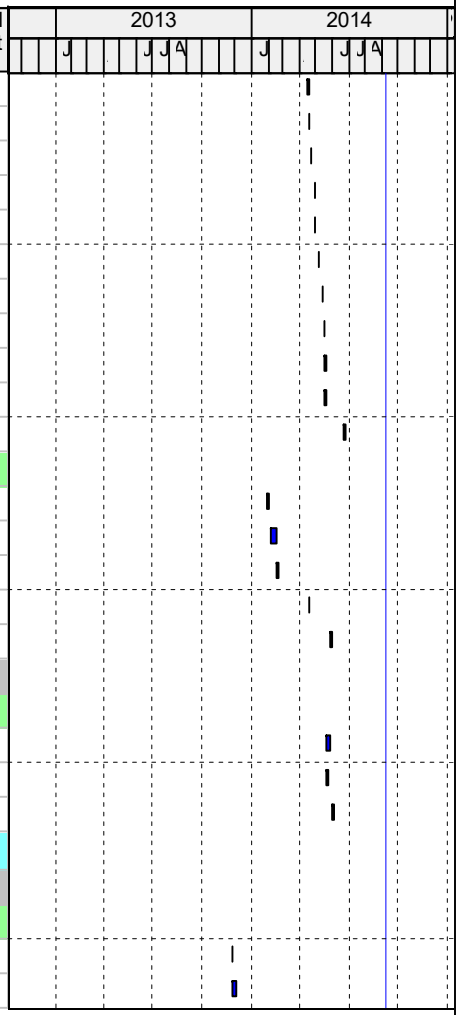



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 04-Dec-13 A | 05-Dec-13 A | |
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 06-Dec-13 A | 09-Dec-13 A | |
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 2 | 0 | 03-Feb-14 A | 04-Feb-14 A | |
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 2 | 0 | 06-Feb-14 A | 07-Feb-14 A | |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 2 | 0 | 07-Feb-14 A | 07-Feb-14 A | |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 2 | 0 | 07-Feb-14 A | 10-Feb-14 A | |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 2 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 2 | 0 | 06-Mar-14 A | 07-Mar-14 A | |
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 2 | 0 | 07-Mar-14 A | 10-Mar-14 A | |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 2 | 0 | 13-Mar-14 A | 14-Mar-14 A | |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 2 | 0 | 08-Apr-14 A | 21-Apr-14 A | |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| S1-4040 | Stair 1 - Set Mtl Stairs / Railings L18 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 10-Dec-13 A | 11-Dec-13 A | |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 12-Dec-13 A | 13-Dec-13 A | |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 16-Dec-13 A | 17-Dec-13 A | |
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 18-Dec-13 A | 19-Dec-13 A | |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 2 | 0 | 12-Feb-14 A | 13-Feb-14 A | |
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 2 | 0 | 13-Feb-14 A | 13-Feb-14 A | |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 2 | 0 | 13-Feb-14 A | 14-Feb-14 A | |

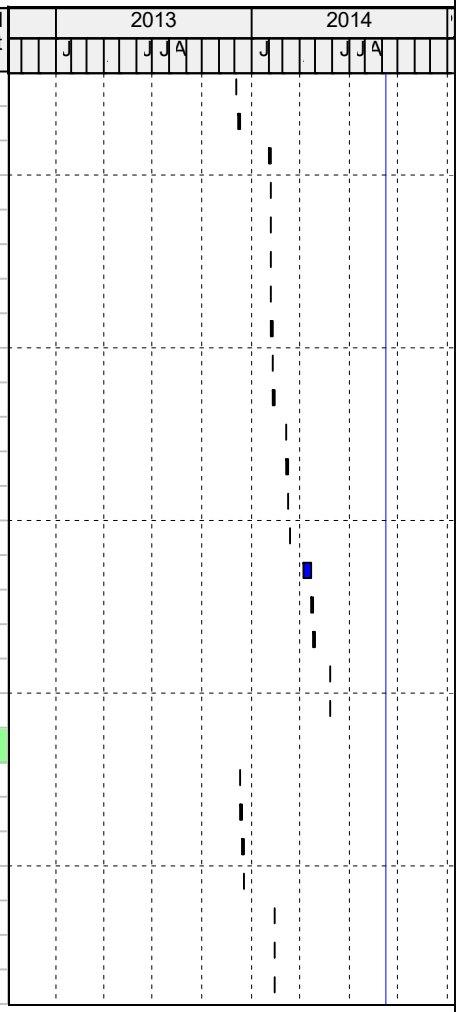



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 2 | 0 | 19-Feb-14 A | 20-Feb-14 A | |
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 2 | 0 | 21-Feb-14 A | 24-Feb-14 A | |
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 2 | 0 | 19-Mar-14 A | 20-Mar-14 A | |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 2 | 0 | 21-Mar-14 A | 22-Mar-14 A | |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 2 | 0 | 14-May-14 A | 15-May-14 A | |
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 2 | 0 | 16-May-14 A | 19-May-14 A | |
| S2-4038 | Stair 2 - Set Mtl Stairs / Railings L17 | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - Set Metal Stairs / Railings LL2 | 6 | 0 | 05-Mar-14 A | 20-Mar-14 A | |
| S3-4002 | Stair 3 - Set Metal Stairs / Railings LL1 | 6 | 0 | 17-Mar-14 A | 21-Mar-14 A | |
| S3-4004 | Stair 3 - Permanent Railings / Final Finishes | 4 | 4 | 03-Nov-14 | 06-Nov-14 | 28 |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |
| S4-4000 | Stair 4 - Set Metal Stairs / Railings LL2 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4002 | Stair 4 - Set Metal Stairs / Railings LL1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4004 | Stair 4 -Set Metal Stairs / Railings L1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4006 | Stair 4 - Permanent Railings / Final Finishes | 4 | 4 | 05-Nov-14 | 11-Nov-14 | 24 |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |
| S6-4000 | Stair 6 - Set Metal Stairs / Railings | 5 | 0 | 25-Jun-14 A | 01-Jul-14 A | |
| S6-4002 | Stair 6 - Permanent Railings / Final Finishes | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 30 |
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |

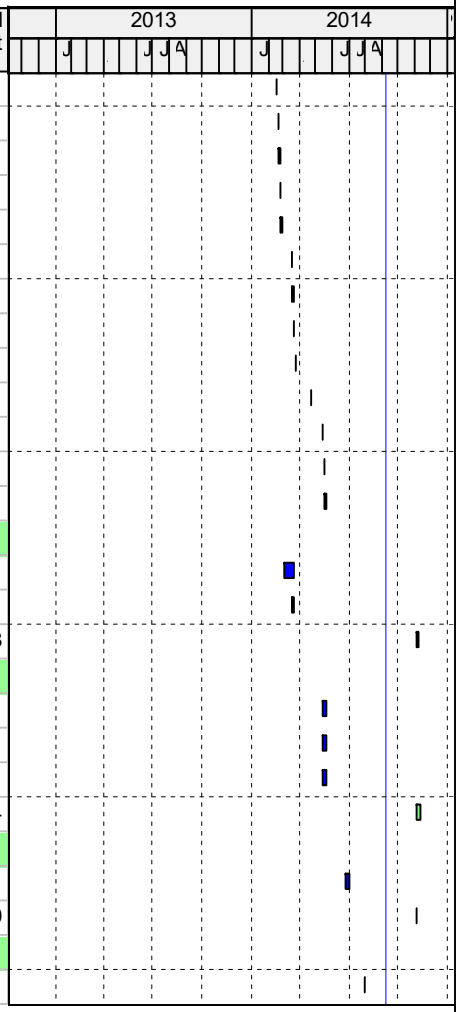



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 8 |
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a -Set Metal Stairs / Railings L1 | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| S4a-4002 | Stair 4a - Permanent Railings / Final Finishes | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 24 |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 07-Jun-13 A | | |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 0 | 17-Jun-13 A | 21-Jun-13 A | |
| EL-1004 | Elev - Submittal Approval | 21 | 0 | 21-Jun-13 A | 01-Jan-14 A | |
| EL-1006 | Elev - Release to Manufacturing | 14 | 0 | 02-Jan-14 A | 15-Jan-14 A | |
| EL-1008 | Elev - Fabrication (Engineered Geared) | 95 | 0 | 16-Jan-14 A | 14-Jun-14 A | |
| EL-1010 | Elev - Machines delivered | 1 | 0 | 12-May-14 A | 12-May-14 A | |
| EL-1011 | Elev - Elevator Machines Flown & Set At Top Of Hoist | 5 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5016 | Elev 5 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-1216 | Elev 1&2 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-3416 | Elev 3&4 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-1202 | Elev 1&2 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-3402 | Elev 3&4 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-5018 | Elev 5 - Set Hoistway Machines | 3 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| EL-1218 | Elev 1&2 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-3418 | Elev 3&4 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-1200 | Elev 1&2 - Hoistway Clear & Ready (GC) | 0 | 0 | 20-Jun-14 A | | |
| EL-1204 | Elev 1&2 - Install Rails & Brackets | 17 | 0 | 23-Jun-14 A | 15-Jul-14 A | |
| EL-3400 | Elev 3&4 - Hoistway Clear & Ready (GC) | 0 | 0 | 23-Jun-14 A | | |

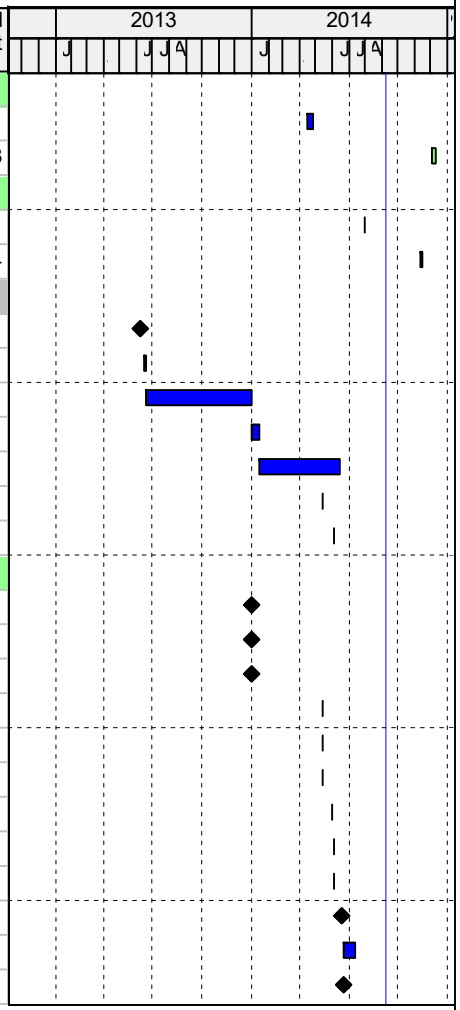


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 24-Jun-14 A | | |
| EL-1206 | Elev 1&2 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Jul-14 A | |
| EL-1207 | Elev 1&2 - Install Pit Equipment/Car Sling/CWT Fram | 3 | 0 | 15-Jul-14 A | 01-Aug-14 A | |
| EL-1208 | Elev 1&2 - Install MHoist & Cable | 5 | 0 | 16-Jul-14 A | 24-Jul-14 A | |
| EL-3407 | Elev 3&4 - Install Pit Equipment/Car Sling/CWT Fram | 5 | 0 | 16-Jul-14 A | 06-Aug-14 A | |
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 21-Jul-14 A | | |
| EL-5004 | Elev 5 - Install Rails & Brackets | 13 | 0 | 21-Jul-14 A | 11-Aug-14 A | |
| EL-3404 | Elev 3&4 - Install Rails & Brackets | 18 | 0 | 23-Jul-14 A | 04-Aug-14 A | |
| EL-3406 | Elev 3&4 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 28-Jul-14 A | |
| EL-3408 | Elev 3&4 - Install Hoist & Cable | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| EL-5007 | Elev 5 - Install Pit Equipment/Car Sling/CWT Frame/V | 5 | 0 | 12-Aug-14 A | 15-Aug-14 A | |
| EL-1210 | Elev 1&2 - Install Entrances/Doors/Fixtures/Fascia | 19 | 16 | 14-Aug-14 A | 29-Sep-14 | 12 |
| EL-3410 | Elev 3&4 - Install Entrances/Doors/Fixtures/Fascia | 30 | 22 | 14-Aug-14 A | 07-Oct-14 | 4 |
| EL-5006 | Elev 5 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Aug-14 A | |
| EL-5008 | Elev 5 - Install MHoist & Cable | 4 | 0 | 18-Aug-14 A | 20-Aug-14 A | |
| EL-5010 | Elev 5 - Install Entrances/Doors/Fixtures/Fascia | 21 | 16 | 21-Aug-14 A | 29-Sep-14 | 12 |
| EL-5012 | Elev 5 - Install Hoistway Equipment/Pipe & Wire | 14 | 14 | 30-Sep-14 | 17-Oct-14 | 12 |
| EL-1212 | Elev 1&2 - Install Hoistway Equipment/Pipe & Wire | 14 | 14 | 30-Sep-14 | 17-Oct-14 | 12 |
| EL-3412 | Elev 3&4 - Install Hoistway Equipment/Pipe & Wire | 23 | 23 | 08-Oct-14 | 07-Nov-14 | 4 |
| EL-5014 | Elev 5 - Install Cab/Wiring/Door Operator(s) | 7 | 7 | 20-Oct-14 | 28-Oct-14 | 12 |
| EL-1214 | Elev 1&2 - Install Cab/Wiring/Door Operator(s) | 7 | 7 | 20-Oct-14 | 28-Oct-14 | 12 |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 1 | 1 | 27-Oct-14* | 27-Oct-14 | 9 |
| EL-6018 | Elev 6 - Set Hoistway Machines | 2 | 2 | 28-Oct-14 | 29-Oct-14 | 9 |
| EL-5022 | Elev 5 - Adjust | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 12 |
| EL-1222 | Elev 1&2 - Adjust | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 12 |
| EL-6016 | Elev 6 - Hoistway Walls Complete (GC) | 0 | 0 | | 29-Oct-14 | 9 |
| EL-6004 | Elev 6 - Install Cylinders/Rails & Brackets | 4 | 4 | 30-Oct-14 | 04-Nov-14 | 9 |

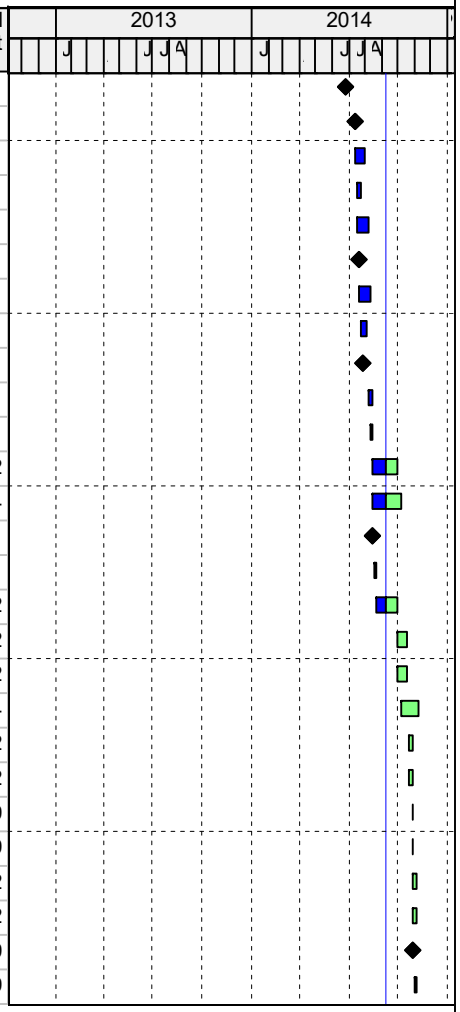


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6006 | Elev 6 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 04-Nov-14 | 9 |
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 12 |
| EL-1224 | Elev 1&2 - Clean / Paint / Punchlist | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 12 |
| EL-6007 | Elev 6 - Install Pit Equipment/Car Sling | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 9 |
| EL-5026 | Elev 5 - Inspections | 7 | 7 | 08-Nov-14 | 14-Nov-14 | 20 |
| EL-1226 | Elev 1&2 - Inspections | 7 | 7 | 08-Nov-14 | 14-Nov-14 | 20 |
| EL-3414 | Elev 3&4 - Install Cab/Wiring/Door Operator(s) | 10 | 10 | 11-Nov-14 | 24-Nov-14 | 4 |
| EL-6010 | Elev 6 - Install Entrances/Doors/Fixtures/Fascia | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 9 |
| EL-6012 | Elev 6 - Install Hoistway Equipment/Pipe & Wire | 2 | 2 | 13-Nov-14 | 14-Nov-14 | 9 |
| EL-6014 | Elev 6 - Install Cab/Wiring/Door Operator(s) | 4 | 4 | 17-Nov-14 | 20-Nov-14 | 9 |
| EL-6022 | Elev 6 - Adjust | 4 | 4 | 21-Nov-14 | 26-Nov-14 | 9 |
| EL-3422 | Elev 3&4 - Adjust | 5 | 5 | 25-Nov-14 | 03-Dec-14 | 4 |
| EL-6024 | Elev 6 - Clean / Paint / Punchlist | 1 | 1 | 01-Dec-14 | 01-Dec-14 | 9 |
| EL-6026 | Elev 6 - Inspections | 1 | 1 | 02-Dec-14 | 02-Dec-14 | 12 |
| EL-3424 | Elev 3&4 - Clean / Paint / Punchlist | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 4 |
| EL-3426 | Elev 3&4 - Inspections | 7 | 7 | 09-Dec-14 | 15-Dec-14 | 6 |
| **Exterior Shell** | | | | | | |
| **Elevations** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2** | | | | | | |
| L3D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Feb-14 A | 12-Feb-14 A | |
| L3-5308 | L3- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 17-Feb-14 A | 21-Feb-14 A | |
| L4D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Feb-14 A | 19-Feb-14 A | |
| L4-5308 | L4- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Feb-14 A | 28-Feb-14 A | |
| L5D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Feb-14 A | 26-Feb-14 A | |
| L5-5308 | L5- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 03-Mar-14 A | 07-Mar-14 A | |
| L6D5308 | Deliver/Stock Wall Panels | 1 | 0 | 05-Mar-14 A | 05-Mar-14 A | |

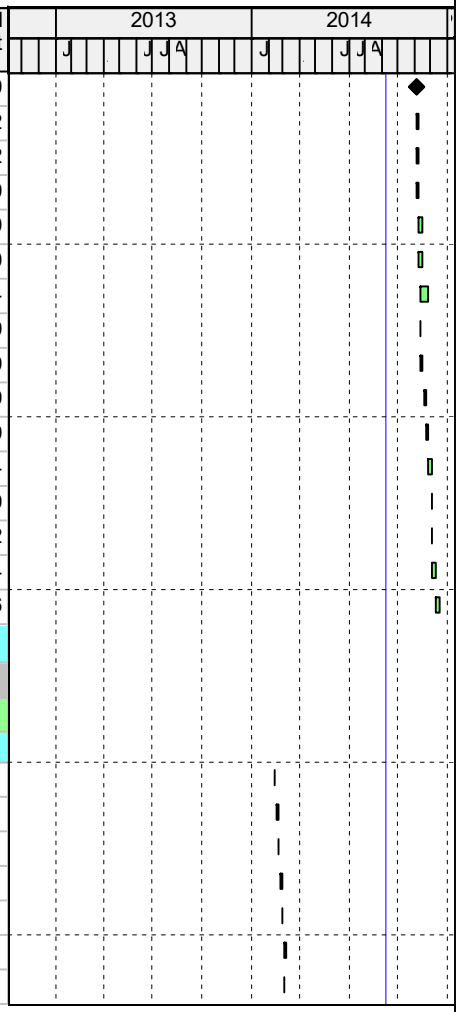



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L6-5308 | L6- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L7-5308 | L7- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L7D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Mar-14 A | 12-Mar-14 A | |
| L8D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Mar-14 A | 19-Mar-14 A | |
| L8-5308 | L8- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Mar-14 A | 28-Mar-14 A | |
| L9D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L9-5308 | L9- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 31-Mar-14 A | 07-Apr-14 A | |
| 10D5308 | Deliver/Stock Wall Panels | 1 | 0 | 02-Apr-14 A | 02-Apr-14 A | |
| L10-5308 | L10- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 07-Apr-14 A | 11-Apr-14 A | |
| 11D5308 | Deliver/Stock Wall Panels | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L11-5308 | L11- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 11-Apr-14 A | 18-Apr-14 A | |
| 12D5308 | Deliver/Stock Wall Panels | 1 | 0 | 16-Apr-14 A | 16-Apr-14 A | |
| L12-5308 | L12- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Apr-14 A | 25-Apr-14 A | |
| 14D5308 | Deliver/Stock Wall Panels | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L14-5308 | L14 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Apr-14 A | 01-May-14 A | |
| 15D5308 | Deliver/Stock Wall Panels | 1 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L15-5308 | L15 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| 16D5308 | Deliver/Stock Wall Panels | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L16-5308 | L16- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| 17D5308 | Deliver/Stock Wall Panels | 1 | 0 | 14-May-14 A | 14-May-14 A | |
| L17-5308 | L17 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 20-May-14 A | 11-Jun-14 A | |
| LL2-5308 | LL2 Thru L4 - Support Frame/Sheathing for Metal Wa | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL1-5308 | LL1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| L1-5308 | L1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| **Level 1** | | | | | | |
| L3-5102 | L3- Storefront Frames | 7 | 6 | 18-Aug-14 A | 19-Sep-14 | 18 |
| L1-5102 | L1 - Storefront Frames | 8 | 4 | 02-Sep-14 A | 11-Sep-14 | 4 |

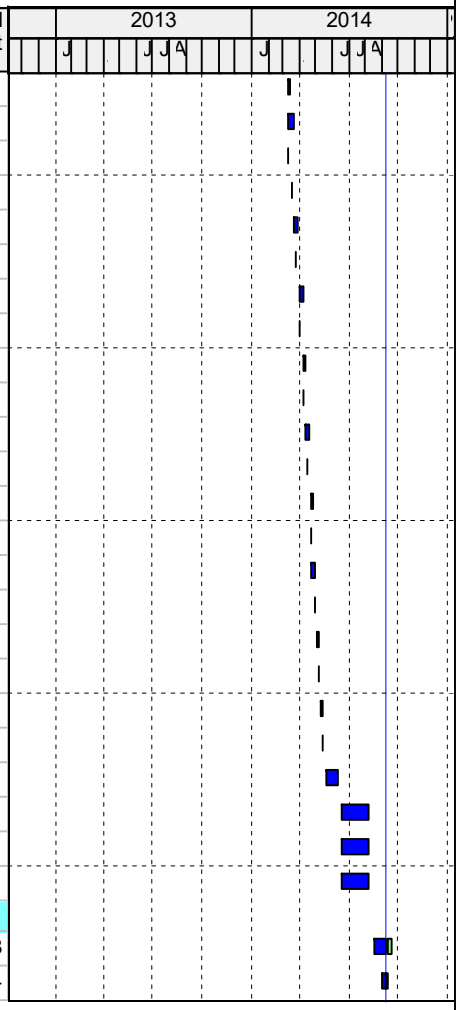


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EP-5110 | L1 - Revolving Doors | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 36 |
| L1-5104 | L1 - Storefront Glazing | 4 | 4 | 03-Oct-14 | 08-Oct-14 | 18 |
| L3-5104 | L3 - Storefront Glazing | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 18 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Levels 3-4** | | | | | | |
| L3-5130 | L3 - Install Punch Windows | 5 | 0 | 24-Feb-14 A | 10-Mar-14 A | |
| L4-5130 | L4 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 12-Mar-14 A | |
| L5-5130 | L5 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L6-5130 | L6- Install Punch Windows | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L7-5130 | L7 - Install Punch Windows | 5 | 0 | 18-Mar-14 A | 21-Mar-14 A | |
| L8-5130 | L8 - Install Punch Windows | 5 | 0 | 24-Mar-14 A | 28-Mar-14 A | |
| L9-5130 | L9 - Install Punch Windows | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L10-5130 | L10 - Install Punch Windows | 5 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-5130 | L11 - Install Punch Windows | 5 | 0 | 14-Apr-14 A | 21-Apr-14 A | |
| L12-5130 | L12 - Install Punch Windows | 5 | 0 | 22-Apr-14 A | 25-Apr-14 A | |
| L14-5130 | L14 - Install Punch Windows | 5 | 0 | 28-Apr-14 A | 05-May-14 A | |
| L15-5130 | L15 - Install Punch Windows | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| L16-5130 | L16 - Install Punch Windows | 5 | 0 | 12-May-14 A | 20-May-14 A | |
| L17-5130 | L17 - Install Punch Windows | 5 | 0 | 27-May-14 A | 16-Jun-14 A | |
| Roofs | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 17 |
| RF-4026 | L1 - City Park - Protection Board | 3 | 3 | 16-Oct-14 | 20-Oct-14 | 17 |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 2 | 21-Oct-14 | 22-Oct-14 | 17 |
| **Pool Membrane - (elev 18')** | | | | | | |
| RF-4034 | Pool - Install plumbing | 3 | 3 | 15-Sep-14* | 17-Sep-14 | 12 |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |

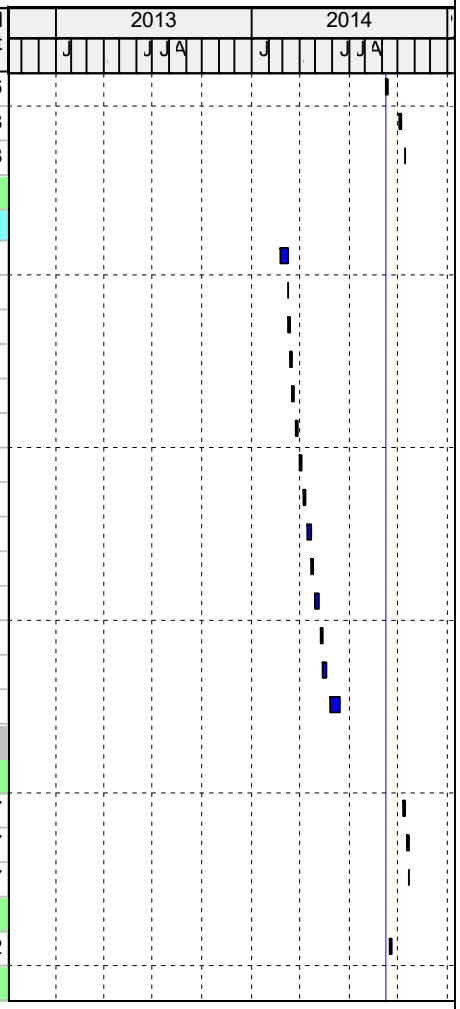



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| RF-4010 | AR - Set Mechanical Equipment | 5 | 0 | 10-Jun-14 A | 12-Jun-14 A | |
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 10 | 0 | 04-Aug-14 A | 27-Aug-14 A | |
| RF-4012 | AR - Coping / Flashing | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 73 |
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 8 | 8 | 15-Sep-14 | 24-Sep-14 | 28 |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |
| PC-4008 | RF - Entry / Porte Cochere Roofing System | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 28 |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | RF - Upper Ballroom Roofing System | 3 | 0 | 28-Jul-14 A | 31-Jul-14 A | |
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 4 | 0 | 31-Jul-14 A | 04-Aug-14 A | |
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |
| RF-4018 | TR - Terrace Roof - Green Roofing System | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 44 |
| RF-4020 | TR - Terrace Roof - Coping / Flashing | 3 | 3 | 02-Oct-14 | 06-Oct-14 | 44 |
| RF-4022 | TR - Terrace Roof - Glass Railing | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 44 |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Perimeter Framing / Sul | 10 | 0 | 02-Jun-14 A | 08-Jul-14 A | |
| RF-4002 | Tower Roof - Roofing System | 10 | 0 | 20-Aug-14 A | 06-Sep-14 A | |
| **PH - Roof - (elev 173')** | | | | | | |
| RF-4030 | PH - Roofing System | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| RF-4032 | PH - Coping / Flashing | 3 | 3 | 08-Sep-14 | 10-Sep-14 | 67 |
| **Rough-In's** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6002 | LL4 - Layout | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| LL4-6008 | LL4 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL4-6012 | LL4 - Fire Sprinkler Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |

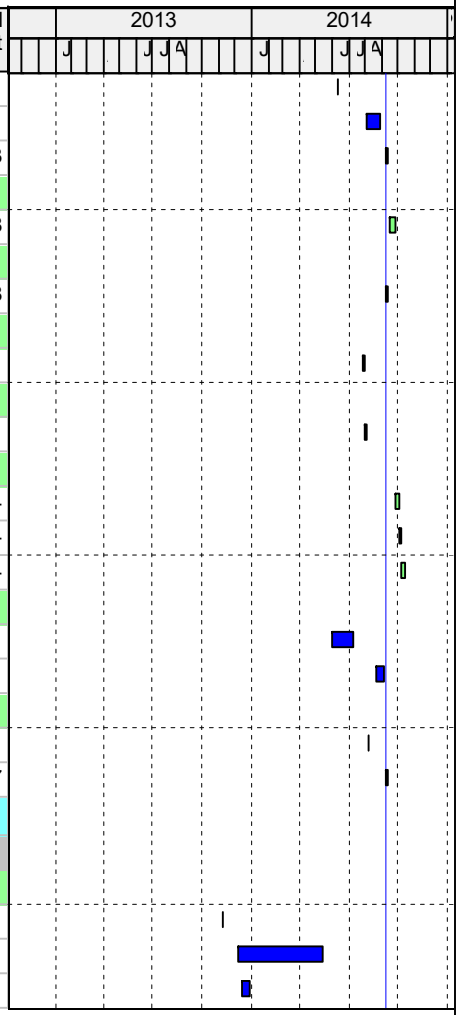


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-6014 | LL4 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6018 | LL4 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6004 | LL4 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL4-6016 | LL4 - Electrical RI | 10 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties RI | 8 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6010 | LL4 - Elevator pits | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| LL4-6020 | LL4 - H Mtl Frames | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL4-6024 | LL4 - Inspections | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 17 |
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6002 | LL3 - Layout | 1 | 0 | 19-Nov-13 A | 19-Nov-13 A | |
| LL3-6008 | LL3 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL3-6012 | LL3 - Fire Sprinkler RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6014 | LL3 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6018 | LL3 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6004 | LL3 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL3-6020 | LL3 - H Mtl Frames | 3 | 0 | 08-May-14 A | 09-May-14 A | |
| LL3-6010 | LL3 - F/P Curbs | 5 | 0 | 19-May-14 A | 19-May-14 A | |
| LL3-6016 | LL3 - Electrical RI | 2 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties RI | 8 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL3-6024 | LL3 - Inspections | 2 | 2 | 12-Sep-14 | 15-Sep-14 | 30 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6002 | LL2 - Layout | 1 | 0 | 14-Jan-14 A | 14-Jan-14 A | |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| LL2-6012 | LL2 - Fire Sprinkler RI | 10 | 0 | 21-Jan-14 A | 03-Feb-14 A | |
| LL2-6014 | LL2 - Plumbing RI | 10 | 0 | 21-Jan-14 A | 14-Feb-14 A | |

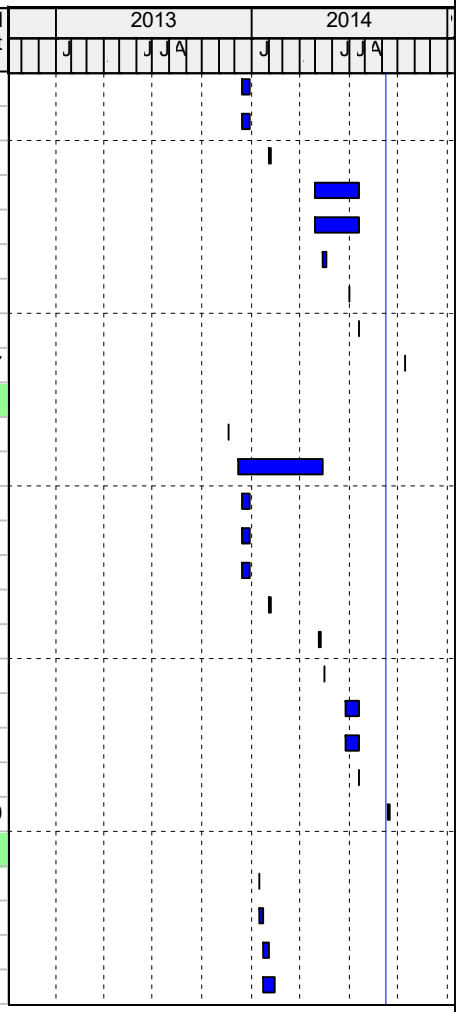



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2E-6016 | LL2 - Electrical RI | 8 | 0 | 03-Feb-14 A | 17-Mar-14 A | |
| LL2-6016 | LL2 - Electrical RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2-6018 | LL2 - HVAC RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2–6004 | LL2 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL2E-6004 | LL2 - CMU Walls | 10 | 0 | 04-Mar-14 A | 09-May-14 A | |
| LL2E-6012 | LL2 - Fire Sprinkler RI | 8 | 0 | 21-Mar-14 A | 01-Apr-14 A | |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 24-Apr-14 A | |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 3 | 0 | 23-Apr-14 A | 21-Jul-14 A | |
| LL2E-6020 | LL2 - H Mtl Frames | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| LL2-6020 | LL2 - H Mtl Frames | 3 | 0 | 12-May-14 A | 13-May-14 A | |
| LL2E-6008 | LL2 - Int Wall Framing | 5 | 0 | 13-May-14 A | 22-Jun-14 A | |
| LL2E-6014 | LL2 - Plumbing RI | 8 | 0 | 13-May-14 A | 30-May-14 A | |
| LL2E-6018 | LL2 - HVAC RI | 8 | 0 | 13-May-14 A | 04-Aug-14 A | |
| LL2E-6022 | LL2 - Fire Alarm / Elec Specialties RI (East of 10) | 8 | 2 | 13-May-14 A | 15-Sep-14 | 43 |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties RI (West of 10) | 8 | 2 | 19-May-14 A | 15-Sep-14 | 35 |
| LL2-6015 | LL2 - Main Elect Room Set Equip / RI - Power to Ma | 15 | 4 | 30-Jun-14 A | 11-Sep-14 | 45 |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 0 | 16-Jul-14 A | 21-Jul-14 A | |
| LL2-6024 | LL2 - Inspections | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 35 |
| LL2-6010 | LL2 - F/P Curbs @ Parking | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 47 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6002 | Layout | 3 | 0 | 03-Jan-14 A | 08-Jan-14 A | |
| LL1-6008 | Int Wall Framing & Inspection | 6 | 0 | 08-Jan-14 A | 21-Jul-14 A | |
| LL1-Z2-6002 | Layout | 3 | 0 | 08-Jan-14 A | 14-Jan-14 A | |
| LL1-Z3-6002 | Layout | 3 | 0 | 14-Jan-14 A | 17-Jan-14 A | |
| LL1-Z2-6008 | Int Wall Framing & Inspection | 6 | 0 | 17-Jan-14 A | 01-Aug-14 A | |
| LL1-Z3-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-Jan-14 A | 04-Aug-14 A | |

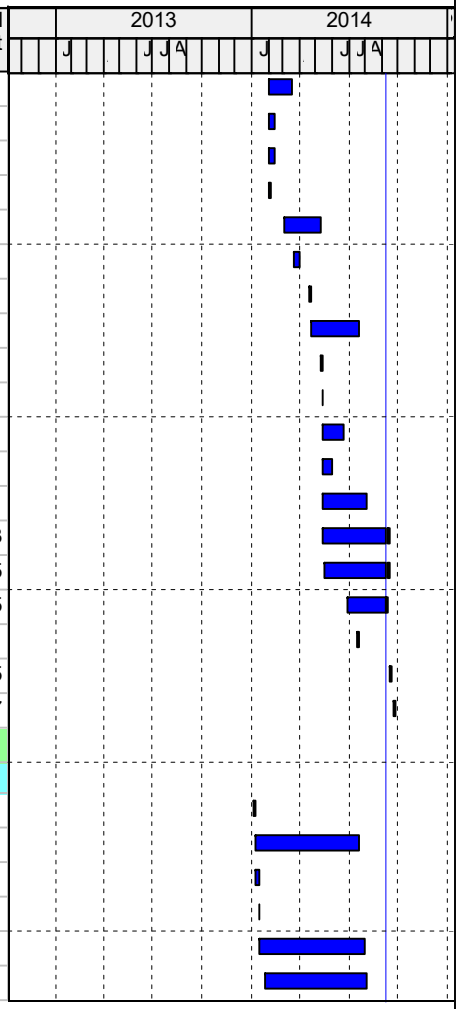


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 09-May-14 A | |
| LL1-Z2-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 28-Apr-14 A | |
| LL1-Z3-6004 | CMU Walls (At All Areas North of Q-Line) | 3 | 0 | 03-Feb-14 A | 13-May-14 A | |
| LL1C-6012 | Complete Fire Sprinkler RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6016 | Complete Electrical RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 10 | 2 | 17-Feb-14 A | 09-Sep-14 | 26 |
| LL1C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 30-Apr-14 A | |
| LL1-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-Z2-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z2-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z3-6012 | Fire Sprinkler RI (At All Areas North of Q-Line) | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z3-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6016 | Electrical RI | 20 | 2 | 17-Feb-14 A | 09-Sep-14 | 15 |
| LL1-Z3-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z2C-6012 | Complete Fire Sprinkler RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6014 | Complete Plumbing RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6016 | Complete Electrical RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 15 | 1 | 24-Feb-14 A | 08-Sep-14 | 19 |
| LL1-Z2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |

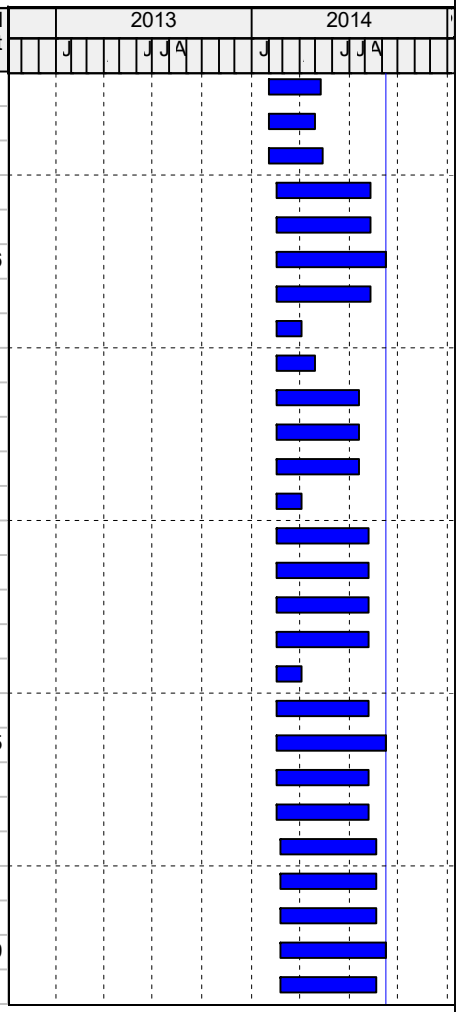


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-6020 | Hollow Metal Door Frames | 5 | 0 | 17-Mar-14 A | 04-Apr-14 A | |
| LL1-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| LL1-Z3-6020 | Hollow Metal Door Frames (At All Areas North of Q-Lir | 1 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| L1B-6004 | CMU Walls [including East Service Corridor] | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L1L-6002 | Layout [including back of house] | 3 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 29-Apr-14 A | |
| L1B-6008 | Int Wall Framing & Inspection | 6 | 0 | 21-Apr-14 A | 08-Aug-14 A | |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 5 | 0 | 25-Apr-14 A | 21-Jul-14 A | |
| LL1C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L1K-6004 | CMU Walls [including public restroom] | 3 | 0 | 05-May-14 A | 08-May-14 A | |
| L1K-6002 | Layout [including public restroom] | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| L1K-6008 | Int Wall Framing & Inspection | 4 | 0 | 09-May-14 A | 22-Aug-14 A | |
| L1B-6002 | Layout [including East Service Corridor] | 3 | 0 | 14-May-14 A | 27-May-14 A | |
| L1L-6008 | Int Wall Framing & Inspection | 6 | 1 | 27-May-14 A | 08-Sep-14 | 0 |
| L1L-6004 | CMU Walls [including back of house] | 3 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L1K-6012 | Fire Sprinkler RI | 10 | 2 | 02-Jun-14 A | 09-Sep-14 | 11 |
| L1K-6014 | Plumbing RI | 10 | 2 | 02-Jun-14 A | 09-Sep-14 | 11 |
| L1K-6016 | Electrical RI | 10 | 2 | 02-Jun-14 A | 09-Sep-14 | 11 |
| L1K-6018 | HVAC RI | 10 | 2 | 02-Jun-14 A | 09-Sep-14 | 11 |
| L1B-6014 | Plumbing RI [including East Service Corridor] | 10 | 0 | 16-Jun-14 A | 24-Jun-14 A | |
| L1B-6018 | HVAC RI | 10 | 0 | 20-Jun-14 A | 15-Aug-14 A | |
| L1B-6012 | Fire Sprinkler RI | 10 | 0 | 21-Jun-14 A | 15-Aug-14 A | |
| L1L-6018 | HVAC RI | 5 | 2 | 23-Jun-14 A | 10-Sep-14 | 0 |
| L1L-6014 | Plumbing RI | 5 | 2 | 24-Jun-14 A | 10-Sep-14 | 0 |
| L1L-6010 | CMU Seismic Clips [including back of house] [DELET | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1L-6012 | Fire Sprinkler RI | 5 | 2 | 25-Jun-14 A | 10-Sep-14 | 0 |
| L1L-6016 | Electrical RI | 5 | 2 | 25-Jun-14 A | 10-Sep-14 | 0 |

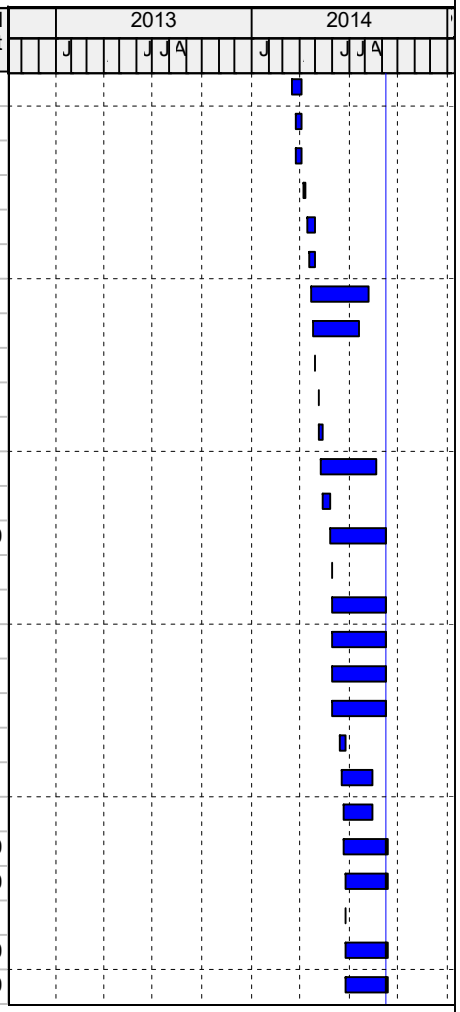


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-6022 | Fire Alarm / Elec Specialties RI | 5 | 2 | 27-Jun-14 A | 10-Sep-14 | 0 |
| L1K-6022 | Fire Alarm / Elec Specialties RI | 10 | 2 | 27-Jun-14 A | 09-Sep-14 | 11 |
| LL1-Z3-6009 | Frame Ceilings [DELETED] | 4 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1B-6016 | Electrical RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| L1B-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| LL1-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-Z2-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L1B-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-6024 | Inspections for Cover | 1 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L1B-6020 | Hollow Metal Door Frames | 5 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| LL1-Z3-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L1K-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 06-Aug-14 A | |
| LL1-Z2-6024 | Inspections for Cover | 2 | 0 | 07-Aug-14 A | 08-Aug-14 A | |
| L1K-6020 | Hollow Metal Door Frames | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-Z2-6009 | Frame Ceilings & Inspection | 6 | 5 | 22-Aug-14 A | 12-Sep-14 | 19 |
| L1L-6020 | Hollow Metal Door Frames | 5 | 1 | 25-Aug-14 A | 08-Sep-14 | 2 |
| LL1-6009 | Frame Ceilings & Inspection (except for bar redesign | 9 | 3 | 02-Sep-14 A | 12-Sep-14 | 31 |
| L1B-6024 | Inspections for Cover | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 3 |
| LL1-Z3-6024 | Inspections for Cover | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 15 |
| L1K-6024 | Inspections for Cover | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 11 |
| L1L-6024 | Inspections for Cover | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 0 |
| L1K-6009 | Frame Ceilings [public restroom] | 3 | 3 | 12-Sep-14 | 16-Sep-14 | 19 |
| L1KC-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 4 | 4 | 15-Sep-14 | 18-Sep-14 | 19 |
| L1KC-6014 | Complete Plumbing RI @ Ceilings & Inspection | 4 | 4 | 15-Sep-14 | 18-Sep-14 | 19 |
| L1KC-6016 | Complete Electrical RI @ Ceilings & Inspection | 4 | 4 | 15-Sep-14 | 18-Sep-14 | 19 |
| L1KC-6018 | Complete HVAC RI @ Ceilings & Inspection | 4 | 4 | 15-Sep-14 | 18-Sep-14 | 19 |
| L1KC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 4 | 4 | 15-Sep-14 | 18-Sep-14 | 19 |

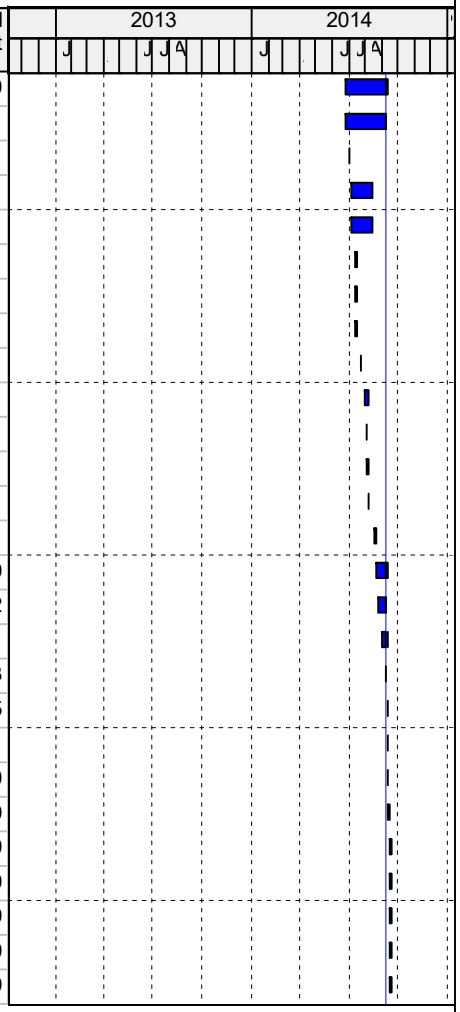


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 15 |
| LL1-Z3C-6014 | Complete Plumbing RI @ Ceilings | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 15 |
| LL1-Z3C-6016 | Complete Electrical RI @ Ceilings | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 15 |
| LL1-Z3C-6018 | Complete HVAC RI @ Ceilings | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 15 |
| LL1-Z3C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 15 |
| L1BC-6012 | Complete Fire Sprinkler RI @ Ceilings | 7 | 7 | 22-Sep-14 | 30-Sep-14 | 3 |
| L1BC-6014 | Complete Plumbing RI @ Ceilings | 7 | 7 | 22-Sep-14 | 30-Sep-14 | 3 |
| L1BC-6018 | Complete HVAC RI @ Ceilings | 7 | 7 | 22-Sep-14 | 30-Sep-14 | 3 |
| L1B-6009 | Frame Ceilings | 7 | 7 | 30-Sep-14 | 08-Oct-14 | 3 |
| L1LC-6012 | Complete Fire Sprinkler RI @ Ceilings | 4 | 4 | 01-Oct-14 | 06-Oct-14 | 0 |
| L1LC-6014 | Complete Plumbing RI @ Ceilings | 4 | 4 | 01-Oct-14 | 06-Oct-14 | 0 |
| L1LC-6016 | Complete Electrical RI @ Ceilings | 4 | 4 | 01-Oct-14 | 06-Oct-14 | 0 |
| L1LC-6018 | Complete HVAC RI @ Ceilings | 4 | 4 | 01-Oct-14 | 06-Oct-14 | 0 |
| L1LC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 4 | 4 | 01-Oct-14 | 06-Oct-14 | 0 |
| L1BC-6016 | Complete Electrical RI @ Ceilings & Inspection | 7 | 7 | 03-Oct-14 | 13-Oct-14 | 3 |
| L1BC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 7 | 7 | 03-Oct-14 | 13-Oct-14 | 3 |
| L1L-6009 | Frame Ceilings & Inspection | 13 | 13 | 06-Oct-14 | 22-Oct-14 | 0 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 0 | 17-Apr-14 A | 09-May-14 A | |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6006 | L2 - Support Frame/Sheathing for Metal Panels | 6 | 0 | 23-Apr-14 A | 07-Aug-14 A | |
| L02-6008 | L2 - Int Wall Framing | 10 | 0 | 25-Apr-14 A | 17-Jul-14 A | |
| L02-6014 | L2 - Plumbing RI | 15 | 0 | 28-Apr-14 A | 07-Aug-14 A | |
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 0 | 28-Apr-14 A | 09-May-14 A | |
| L02-6004 | L2 - CMU Walls | 5 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L02-6002 | L2 - Layout | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 0 | 19-May-14 A | 19-May-14 A | |

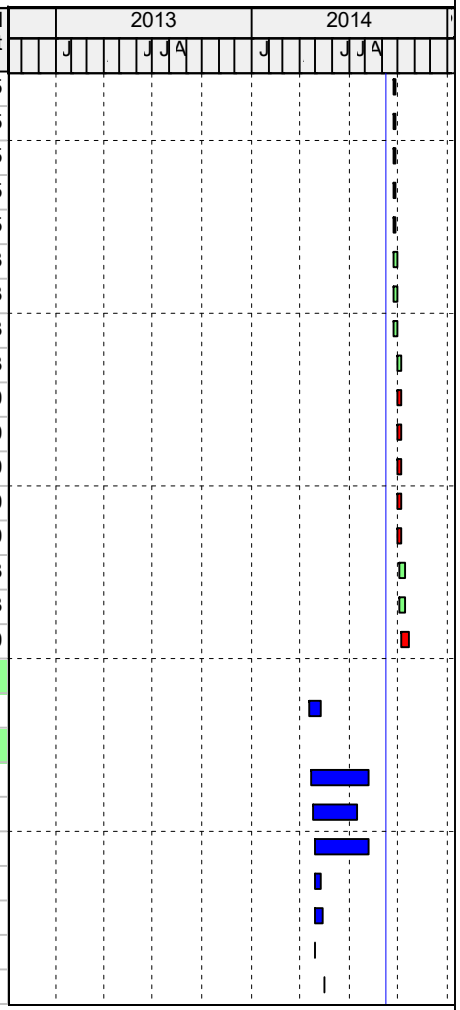


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-6018 | L2 - HVAC RI (including equipment) | 20 | 7 | 18-Jun-14 A | 16-Sep-14 | 27 |
| L02-6016 | L2 - Electrical RI | 10 | 0 | 24-Jun-14 A | 14-Aug-14 A | |
| L02-6022 | L2 - Fire Alarm / Elec Specialties RI | 10 | 1 | 24-Jun-14 A | 08-Sep-14 | 38 |
| L02-6012 | L2 - Fire Sprinkler RI | 10 | 0 | 26-Jun-14 A | 07-Aug-14 A | |
| L02-6020 | L2 - H Mtl Frames | 5 | 0 | 11-Jul-14 A | 17-Jul-14 A | |
| L02-6024 | L2 - Inspections | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 27 |
| Upper Tower - (Levels 3 thru PH) | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L07-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 01-Apr-11 A | 11-Apr-11 A | |
| L04-6012 | Fire Sprinkler Mains | 5 | 0 | 01-Feb-14 A | 03-Apr-14 A | |
| L03-8219 | HVAC Risers | 5 | 0 | 11-Feb-14 A | 23-Mar-14 A | |
| L03-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 11-Feb-14 A | 03-Mar-14 A | |
| L03-6002 | Layout | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| L04-8219 | HVAC Risers | 5 | 0 | 13-Feb-14 A | 23-Mar-14 A | |
| L05-8219 | HVAC Risers | 5 | 0 | 17-Feb-14 A | 03-Mar-14 A | |
| L03-6008 | Frame Shaft Walls | 3 | 0 | 18-Feb-14 A | 26-Mar-14 A | |
| L04-6002 | Layout | 5 | 0 | 19-Feb-14 A | 25-Feb-14 A | |
| L04-6008 | Frame Shaft Walls | 3 | 0 | 20-Feb-14 A | 26-Mar-14 A | |
| L03-6011 | PreRock Shafts | 2 | 0 | 24-Feb-14 A | 25-Mar-14 A | |
| L03-6010 | Frame Walls | 5 | 0 | 25-Feb-14 A | 25-Mar-14 A | |
| L05-6002 | Layout | 5 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| L04-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 28-Feb-14 A | 05-Mar-14 A | |
| L03-6016 | Electrical RI | 5 | 0 | 03-Mar-14 A | 04-Apr-14 A | |
| L03-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 12-Mar-14 A | |
| L04-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 13-Mar-14 A | |
| L04-6010 | Frame Walls | 5 | 0 | 04-Mar-14 A | 05-Jun-14 A | |
| L05-6008 | Frame Shaft Walls | 3 | 0 | 05-Mar-14 A | 27-Mar-14 A | |

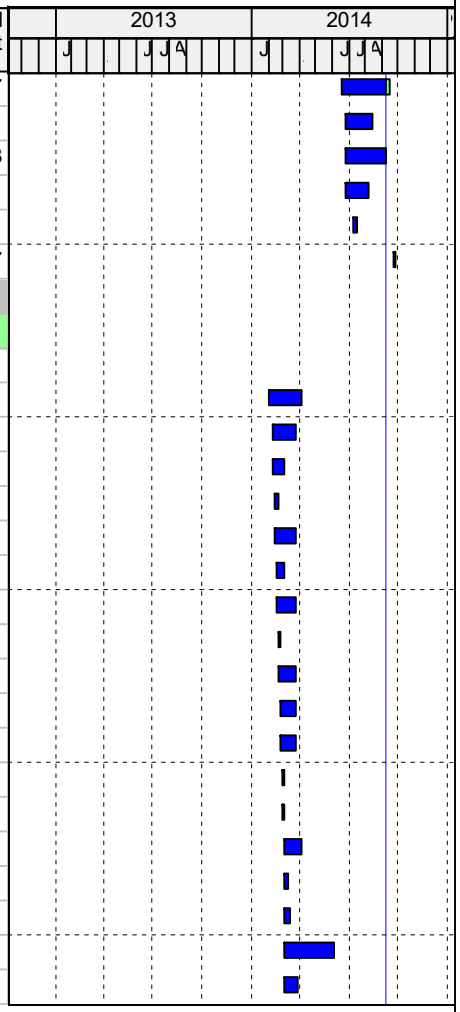



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L07-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L05-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 06-Mar-14 A | 21-Mar-14 A | |
| L03-6020 | Install Hollow Metal Frames | 3 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L04-6020 | Install Hollow Metal Frames | 3 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L05-6010 | Frame Walls | 5 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L06-6002 | Layout | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L04-6011 | PreRock Shafts | 2 | 0 | 18-Mar-14 A | 25-Mar-14 A | |
| L05-6009 | Inspect Shafts | 1 | 0 | 18-Mar-14 A | 18-Mar-14 A | |
| L05-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| L06-6008 | Frame Shaft Walls | 3 | 0 | 19-Mar-14 A | 03-Apr-14 A | |
| L06-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 27-Mar-14 A | |
| L04-6016 | Electrical RI | 5 | 0 | 20-Mar-14 A | 09-Apr-14 A | |
| L05-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 26-Mar-14 A | |
| L06-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 07-Apr-14 A | |
| L07-6002 | Layout | 5 | 0 | 24-Mar-14 A | 30-Apr-14 A | |
| L03-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L03-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L05-6016 | Electrical RI | 5 | 0 | 25-Mar-14 A | 05-Jun-14 A | |
| L04-6019 | Complete Top Out GWB | 2 | 0 | 26-Mar-14 A | 06-Jun-14 A | |
| L05-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L06-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| L03-6019 | Complete Top Out GWB | 2 | 0 | 27-Mar-14 A | 02-May-14 A | |
| L08-6002 | Layout | 5 | 0 | 27-Mar-14 A | 02-Apr-14 A | |
| L05-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 28-Mar-14 A | 03-Apr-14 A | |

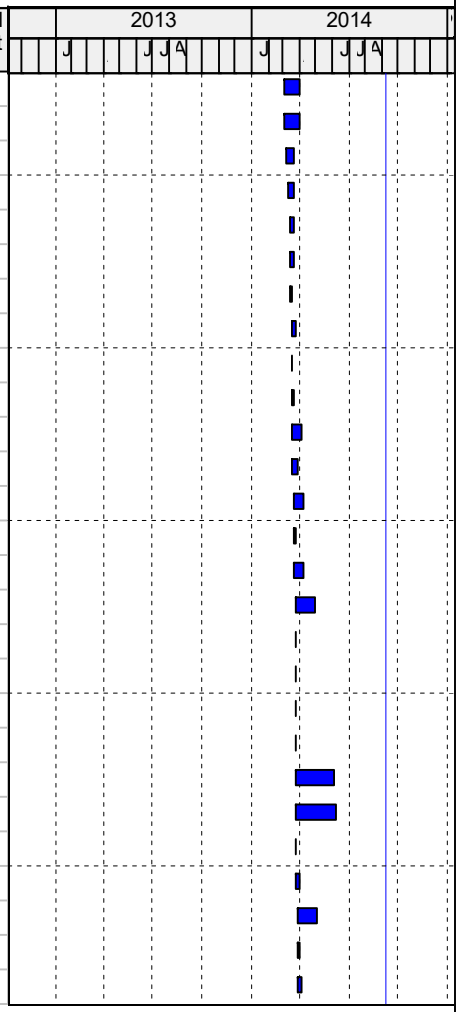



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-6010 | Frame Walls | 5 | 0 | 28-Mar-14 A | 07-Apr-14 A | |
| L03-6012 | Fire Sprinkler Mains | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L07-6008 | Frame Shaft Walls | 3 | 0 | 31-Mar-14 A | 03-Apr-14 A | |
| L05-6019 | Complete Top Out GWB | 2 | 0 | 01-Apr-14 A | 08-Apr-14 A | |
| L08-6008 | Frame Shaft Walls | 3 | 0 | 02-Apr-14 A | 21-Apr-14 A | |
| L03-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L04-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L05-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L06-6016 | Electrical RI | 5 | 0 | 03-Apr-14 A | 15-Apr-14 A | |
| L07-6009 | Inspect Shafts | 1 | 0 | 03-Apr-14 A | 03-Apr-14 A | |
| L07-6011 | PreRock Shafts | 2 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| L05-6012 | Fire Sprinkler Mains | 5 | 0 | 04-Apr-14 A | 30-Apr-14 A | |
| L06-6012 | Fire Sprinkler Mains | 5 | 0 | 07-Apr-14 A | 30-Apr-14 A | |
| L06-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L06-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L07-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| L07-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L03-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L03-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L04-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L06-6009 | Inspect Shafts | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L06-6019 | Complete Top Out GWB | 2 | 0 | 08-Apr-14 A | 18-Apr-14 A | |
| L07-6010 | Frame Walls | 5 | 0 | 08-Apr-14 A | 15-Apr-14 A | |
| L08-6011 | PreRock Shafts | 2 | 0 | 08-Apr-14 A | 23-Apr-14 A | |
| L09-6002 | Layout | 5 | 0 | 08-Apr-14 A | 26-Apr-14 A | |
| L03-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 09-Apr-14 A | 08-May-14 A | |
| L03-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |

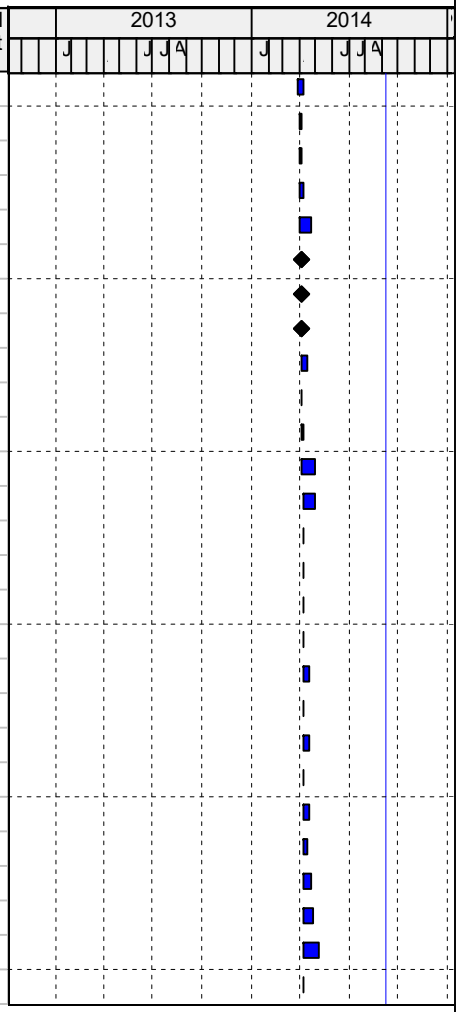



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 09-Apr-14 A | 14-Apr-14 A | |
| L08-6009 | Inspect Shafts | 1 | 0 | 09-Apr-14 A | 25-Apr-14 A | |
| L09-6008 | Frame Shaft Walls | 3 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| L08-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| L04-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 15-Apr-14 A | 16-Apr-14 A | |
| L07-6012 | Fire Sprinkler Mains | 5 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| L07-6016 | Electrical RI | 5 | 0 | 15-Apr-14 A | 12-May-14 A | |
| L07-6020 | Install Hollow Metal Frames | 3 | 0 | 16-Apr-14 A | 23-Apr-14 A | |
| L05-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 17-Apr-14 A | 25-Apr-14 A | |
| L06-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 17-Apr-14 A | 12-May-14 A | |
| L06-6023 | Inspection of Exterior Framing | 0 | 0 | 17-Apr-14 A | | |
| L09-8219 | HVAC Risers | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L09-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L04-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 18-Apr-14 A | 20-Apr-14 A | |
| L04-6028 | PreRock at Heat Pumps | 2 | 0 | 20-Apr-14 A | 22-Apr-14 A | |
| L08-8219 | HVAC Risers | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6009 | Inspect Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6011 | PreRock Shafts | 2 | 0 | 22-Apr-14 A | 24-Apr-14 A | |
| L04-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L06-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 23-Apr-14 A | 25-Apr-14 A | |
| L08-6020 | Install Hollow Metal Frames | 3 | 0 | 23-Apr-14 A | 13-May-14 A | |
| L11-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L11-8220 | Plumbing Risers - Install | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L04-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L09-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |

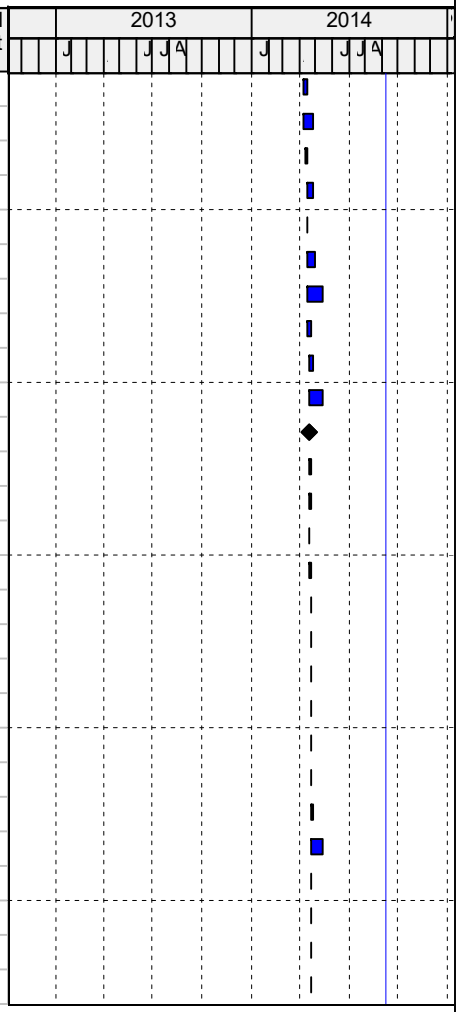



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L10-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 20-May-14 A | |
| L12-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L04-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 25-Apr-14 A | 11-Jun-14 A | |
| L04-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L09-6010 | Frame Walls | 5 | 0 | 25-Apr-14 A | 20-May-14 A | |
| L09-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L10-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L11-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 30-Apr-14 A | |
| L12-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L08-6010 | Frame Walls | 5 | 0 | 26-Apr-14 A | 30-Apr-14 A | |
| L10-6002 | Layout | 5 | 0 | 27-Apr-14 A | 27-Apr-14 A | |
| L04-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 28-Apr-14 A | 30-Apr-14 A | |
| L05-6018 | HVAC RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6028 | PreRock at Heat Pumps | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L07-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 28-Apr-14 A | 12-May-14 A | |
| L10-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-Apr-14 A | 22-May-14 A | |
| L11-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L12-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L05-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| L05-6028 | PreRock at Heat Pumps | 2 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |

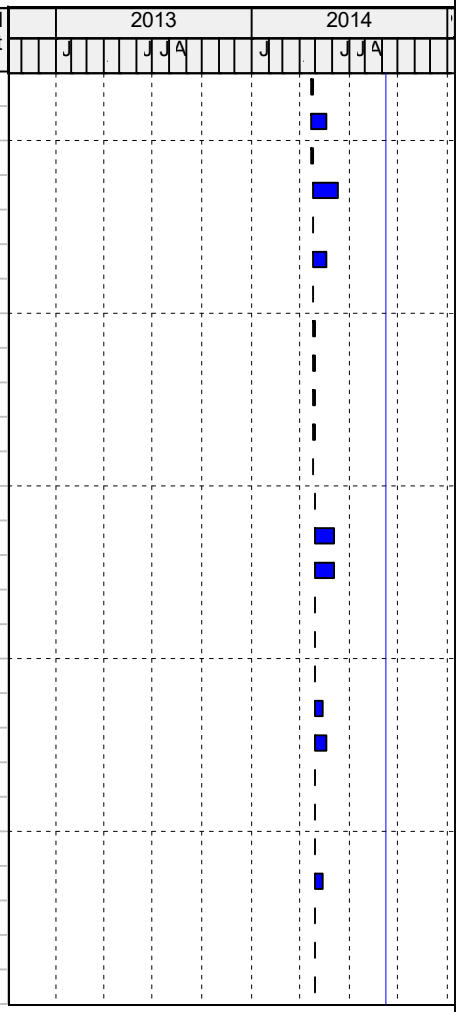


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 09-May-14 A | |
| L06-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L06-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L08-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L08-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L09-6020 | Install Hollow Metal Frames | 3 | 0 | 29-Apr-14 A | 20-May-14 A | |
| L09-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L10-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L04-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 30-Apr-14 A | 02-May-14 A | |
| L09-6019 | Complete Top Out GWB | 2 | 0 | 30-Apr-14 A | 06-Jun-14 A | |
| L11-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L12-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L03-6028 | PreRock at Heat Pumps | 2 | 0 | 01-May-14 A | 02-May-14 A | |
| L05-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L06-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L03-6014 | Set Tubs & Plumbing RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L05-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L05-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| L06-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L06-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 09-May-14 A | |
| L03-6018 | HVAC RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L03-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 06-May-14 A | 06-May-14 A | |
| L07-6014 | Set Tubs & Plumbing RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |

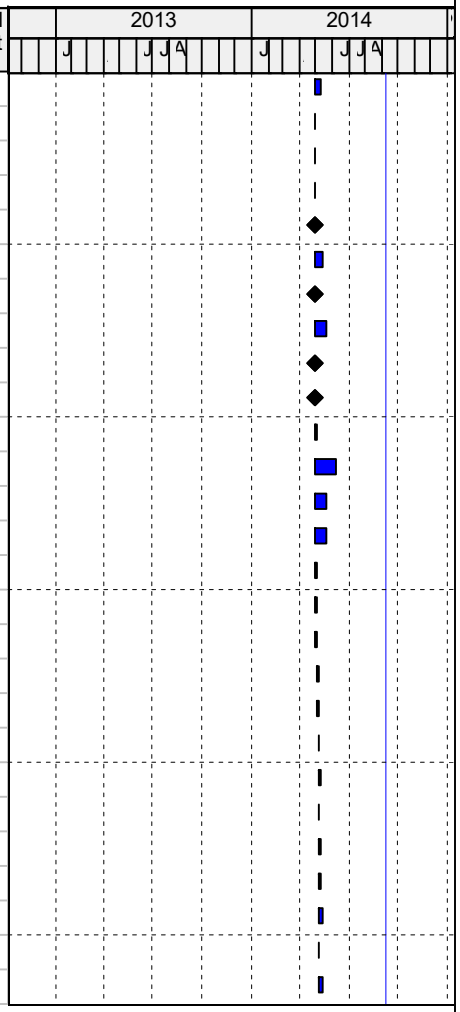



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 06-May-14 A | 09-May-14 A | |
| L03-6004 | CMU Wall/Clips | 3 | 0 | 07-May-14 A | 08-May-14 A | |
| L03-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L03-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 08-May-14 A | 13-May-14 A | |
| L03-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6004 | CMU Walls | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6018 | HVAC RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L11-6010 | Frame Walls | 5 | 0 | 09-May-14 A | 15-May-14 A | |
| L05-6014 | Set Tubs & Plumbing RI | 5 | 0 | 12-May-14 A | 05-Jun-14 A | |
| L07-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 12-May-14 A | 13-May-14 A | |
| L11-6020 | Install Hollow Metal Frames | 3 | 0 | 12-May-14 A | 14-May-14 A | |
| L11-6019 | Complete Top Out GWB | 2 | 0 | 12-May-14 A | 14-May-14 A | |
| L14-6002 | Layout | 5 | 0 | 12-May-14 A | 14-May-14 A | |
| L15-6002 | Layout | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L05-6004 | CMU Walls | 3 | 0 | 13-May-14 A | 13-May-14 A | |
| L06-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 25-Jun-14 A | |
| L06-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 13-May-14 A | 14-Jul-14 A | |
| L07-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 05-Jun-14 A | |
| L07-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| L07-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 13-May-14 A | 13-May-14 A | |
| L14-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L16-6002 | Layout | 5 | 0 | 13-May-14 A | 16-May-14 A | |
| L06-6004 | CMU Walls | 3 | 0 | 14-May-14 A | 14-May-14 A | |
| L07-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 15-May-14 A | |

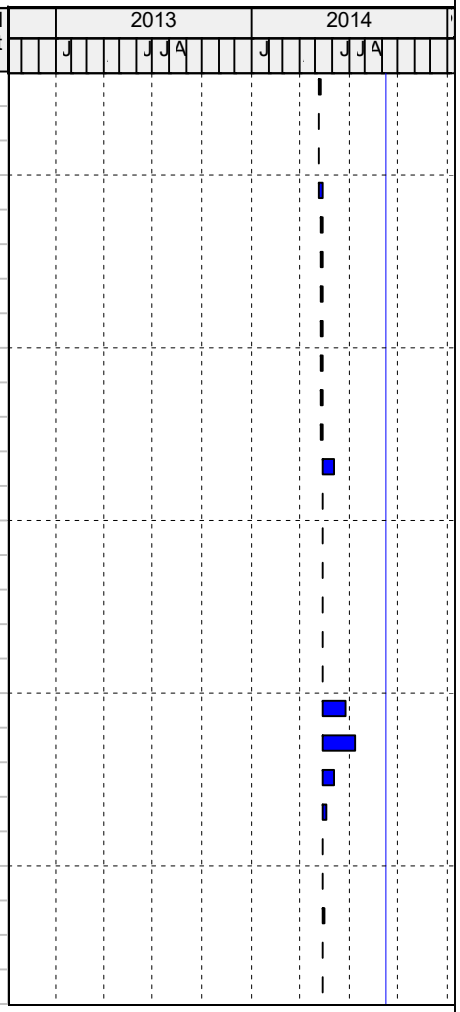



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-6012 | Fire Sprinkler Mains | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6002 | Layout | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L07-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6014 | Set Tubs & Plumbing RI | 5 | 0 | 16-May-14 A | 25-Jun-14 A | |
| L08-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L11-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L12-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L07-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L08-6028 | PreRock at Heat Pumps | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L09-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L10-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L11-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L15-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 19-May-14 A | 19-May-14 A | |
| L07-6028 | PreRock at Heat Pumps | 2 | 0 | 20-May-14 A | 21-May-14 A | |
| L07-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L08-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 20-May-14 A | 21-May-14 A | |
| L10-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L11-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L14-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L07-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 21-May-14 A | 27-May-14 A | |
| L08-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 21-May-14 A | 21-May-14 A | |

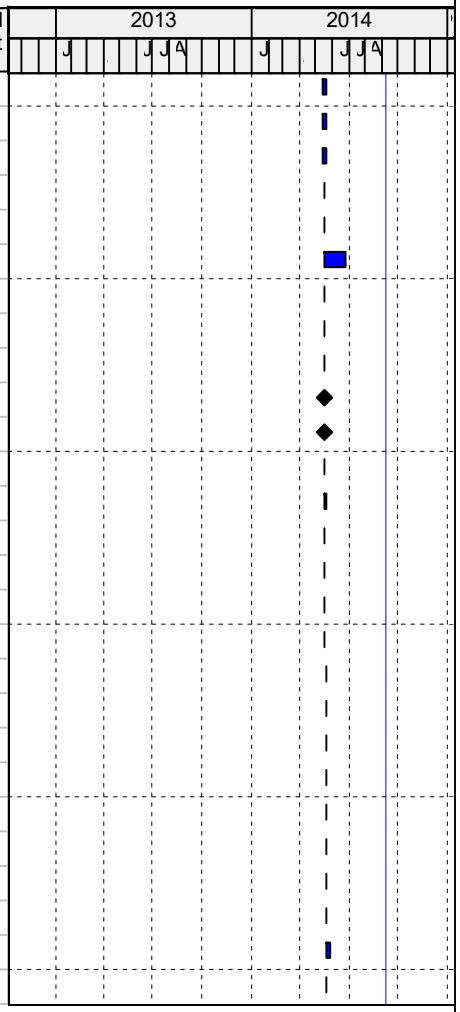



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L09-6028 | PreRock at Heat Pumps | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L10-6014 | Set Tubs & Plumbing RI | 5 | 0 | 21-May-14 A | 27-Jun-14 A | |
| L10-6010 | Frame Walls | 5 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6019 | Complete Top Out GWB | 2 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L11-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L12-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L14-8220 | Plumbing Risers - Install | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L15-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L16-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L07-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| L08-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 22-May-14 A | 22-May-14 A | |
| L10-6012 | Fire Sprinkler Mains | 5 | 0 | 22-May-14 A | 27-May-14 A | |
| L08-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L09-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6020 | Install Hollow Metal Frames | 3 | 0 | 23-May-14 A | 03-Jun-14 A | |
| L10-6028 | PreRock at Heat Pumps | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L14-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L15-8220 | Plumbing Risers - Install | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L09-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 27-May-14 A | 27-May-14 A | |
| L12-6010 | Frame Walls | 5 | 0 | 27-May-14 A | 02-Jun-14 A | |
| L08-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L09-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 28-May-14 A | 28-May-14 A | |
| L10-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 28-May-14 A | 03-Jun-14 A | |
| L14-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L15-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-May-14 A | 30-May-14 A | |

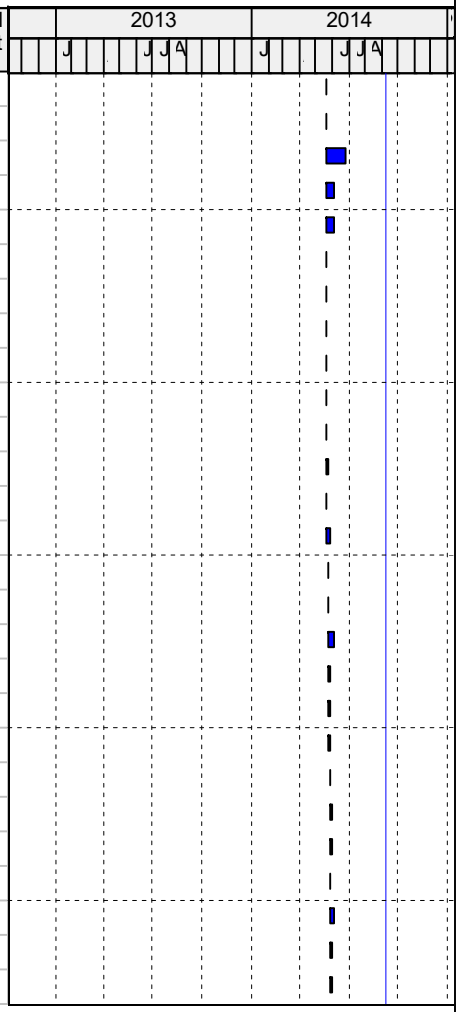



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 28-May-14 A | 28-May-14 A | |
| L16-8220 | Plumbing Risers - Install | 2 | 0 | 28-May-14 A | 29-May-14 A | |
| L08-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 29-May-14 A | 30-May-14 A | |
| L10-6016 | Electrical RI | 5 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L10-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| L12-6012 | Fire Sprinkler Mains | 5 | 0 | 30-May-14 A | 26-Jun-14 A | |
| L12-6020 | Install Hollow Metal Frames | 3 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L15-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L17-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L17-8220 | Plumbing Risers - Install | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L10-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L11-6016 | Electrical RI | 5 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L11-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L12-6019 | Complete Top Out GWB | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L14-6020 | Install Hollow Metal Frames | 3 | 0 | 02-Jun-14 A | 05-Jun-14 A | |
| L14-6010 | Frame Walls | 5 | 0 | 02-Jun-14 A | 04-Jun-14 A | |
| L16-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| L14-6019 | Complete Top Out GWB | 2 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L16-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L10-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| L17-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 04-Jun-14 A | 11-Jun-14 A | |
| L08-6016 | Electrical RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L08-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L09-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L12-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |

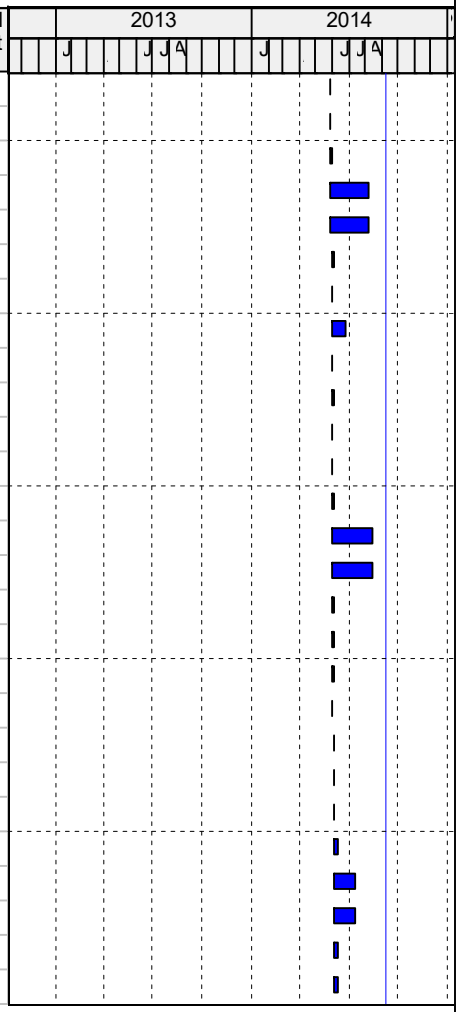


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6010 | Frame Walls | 3 | 0 | 05-Jun-14 A | 11-Jun-14 A | |
| L09-6012 | Fire Sprinkler Mains | 5 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L09-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L11-6012 | Fire Sprinkler Mains | 4 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L12-6014 | Set Tubs & Plumbing RI | 4 | 0 | 06-Jun-14 A | 27-Jun-14 A | |
| L11-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jun-14 A | 11-Jun-14 A | |
| L09-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-Jun-14 A | 25-Jun-14 A | |
| L14-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L15-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L16-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L09-6016 | Electrical RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L14-6014 | Set Tubs & Plumbing RI | 4 | 0 | 10-Jun-14 A | 21-Jul-14 A | |
| L15-6020 | Install Hollow Metal Frames | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L15-6019 | Complete Top Out GWB | 2 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6014 | Set Tubs & Plumbing RI | 4 | 0 | 11-Jun-14 A | 26-Jun-14 A | |
| L11-6028 | PreRock at Heat Pumps | 2 | 0 | 13-Jun-14 A | 14-Jun-14 A | |
| L11-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 14-Jun-14 A | 14-Jun-14 A | |
| L14-6012 | Fire Sprinkler Mains | 2 | 0 | 16-Jun-14 A | 27-Jun-14 A | |
| L14-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 0 | 18-Jun-14 A | 18-Jun-14 A | |
| L15-6023 | Inspection of Exterior Framing | 0 | 0 | 18-Jun-14 A | | |
| L17-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 18-Jun-14 A | 23-Jun-14 A | |
| L17-6010 | Frame Walls | 5 | 0 | 18-Jun-14 A | 29-Jul-14 A | |
| L10-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L12-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 20-Jun-14 A | |

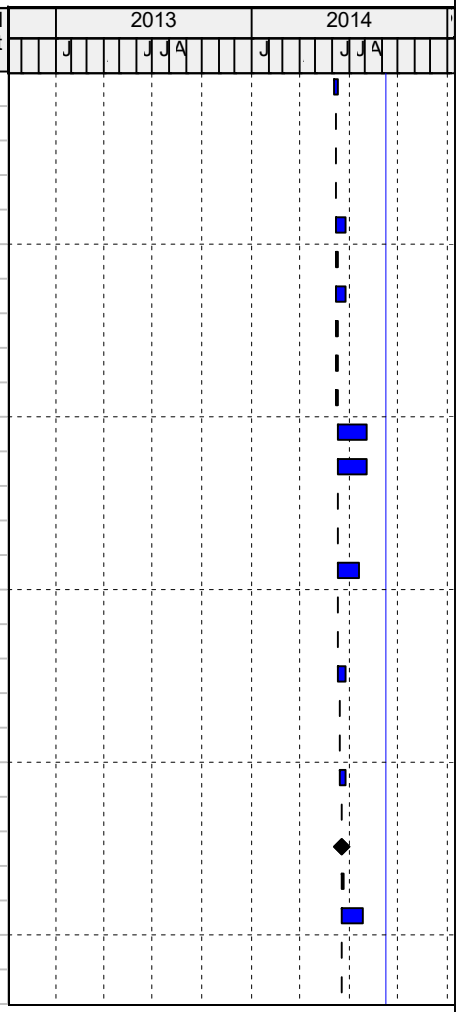



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6023 | Inspection of Exterior Framing | 0 | 0 | 20-Jun-14 A | | |
| L15-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 0 | 20-Jun-14 A | 20-Jun-14 A | |
| L10-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-Jun-14 A | 23-Jun-14 A | |
| L15-6014 | Set Tubs & Plumbing RI | 5 | 0 | 22-Jun-14 A | 24-Jul-14 A | |
| L08-6018 | HVAC RI | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L12-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L14-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L15-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L08-6221 | Frame Unit Ceilings | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| L11-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 24-Jun-14 A | 27-Jun-14 A | |
| L12-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L14-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6023 | Inspection of Exterior Framing | 0 | 0 | 24-Jun-14 A | | |
| L12-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| L12-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L14-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L15-6012 | Fire Sprinkler Mains | 2 | 0 | 25-Jun-14 A | 22-Jul-14 A | |
| L16-6023 | Inspection of Exterior Framing | 0 | 0 | 25-Jun-14 A | | |
| L03-6024 | Inspections for GWB Cover | 1 | 0 | 27-Jun-14 A | 27-Jun-14 A | |
| L09-6018 | HVAC RI | 3 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L09-6221 | Frame Unit Ceilings | 2 | 0 | 27-Jun-14 A | 30-Jun-14 A | |
| L12-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L14-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L15-6028 | PreRock at Heat Pumps | 2 | 0 | 30-Jun-14 A | 01-Jul-14 A | |

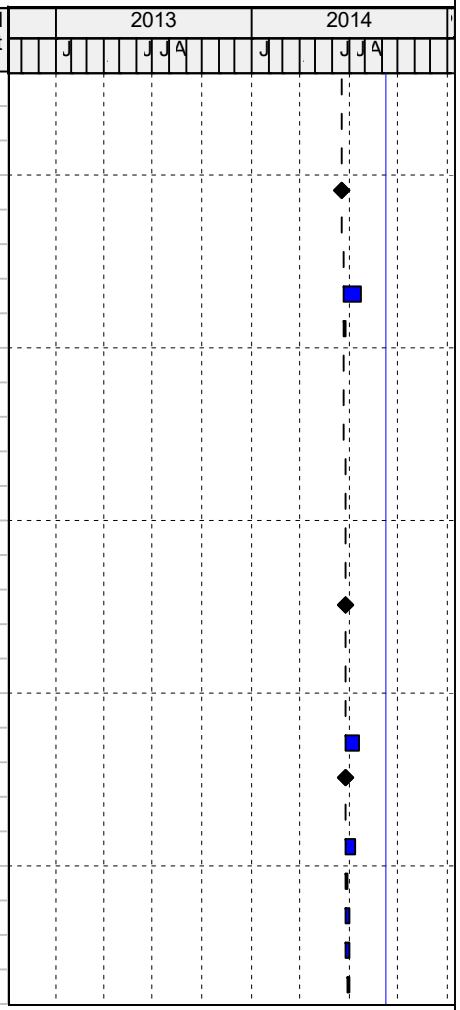


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 30-Jun-14 A | 30-Jun-14 A | |
| L16-6010 | Frame Walls | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| L16-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L15-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L15-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L04-6024 | Inspections for GWB Cover | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L10-6018 | HVAC RI | 3 | 0 | 07-Jul-14 A | 21-Jul-14 A | |
| L11-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L15-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L16-6012 | Fire Sprinkler Mains | 2 | 0 | 07-Jul-14 A | 24-Jul-14 A | |
| L16-6020 | Install Hollow Metal Frames | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L16-6028 | PreRock at Heat Pumps | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L17-6019 | Complete Top Out GWB | 1 | 0 | 07-Jul-14 A | 08-Aug-14 A | |
| L11-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L15-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 08-Jul-14 A | 04-Aug-14 A | |
| L17-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jul-14 A | 01-Aug-14 A | |
| L10-6221 | Frame Unit Ceilings | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| L17-6012 | Fire Sprinkler Mains | 2 | 0 | 09-Jul-14 A | 12-Aug-14 A | |
| L05-6024 | Inspections for GWB Cover | 2 | 0 | 10-Jul-14 A | 10-Jul-14 A | |
| L04-6000 | Tape/Finish GWB | 6 | 0 | 11-Jul-14 A | 23-Jul-14 A | |
| L16-6019 | Complete Top Out GWB | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L16-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L15-6018 | HVAC RI | 3 | 0 | 16-Jul-14 A | 18-Jul-14 A | |
| L16-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-6024 | Inspections for GWB Cover | 2 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6018 | HVAC RI | 3 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L16-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |

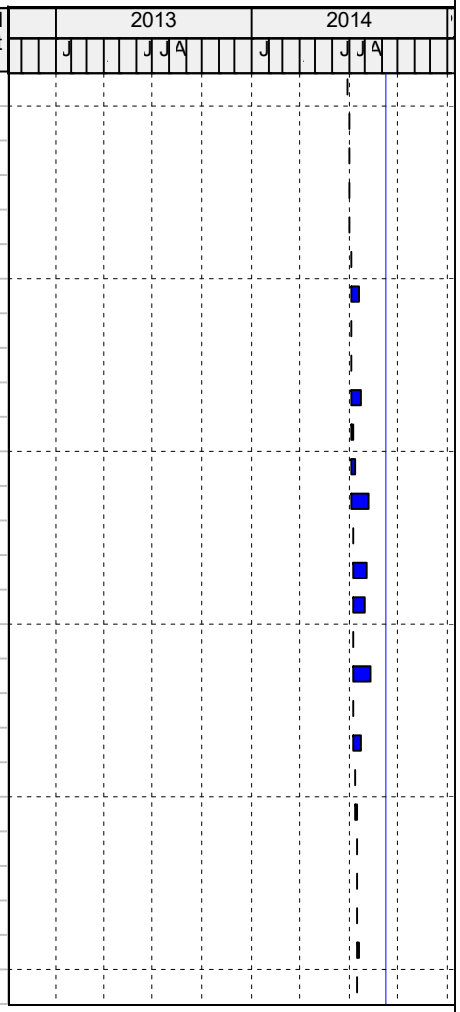



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 21-Jul-14 A | 18-Aug-14 A | |
| L15-6013 | Fire Sprinkler Branch Lines | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| L03-6000 | Tape/Finish GWB | 6 | 0 | 23-Jul-14 A | 29-Jul-14 A | |
| L11-6018 | HVAC RI | 3 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L15-6221 | Frame Unit Ceilings | 2 | 0 | 23-Jul-14 A | 01-Aug-14 A | |
| L16-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L17-6020 | Install Hollow Metal Frames | 3 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| L11-6221 | Frame Unit Ceilings | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L12-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L14-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L14-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L16-6014 | Set Tubs & Plumbing RI | 5 | 0 | 28-Jul-14 A | 18-Aug-14 A | |
| L07-6024 | Inspections for GWB Cover | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L12-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L05-6000 | Tape/Finish GWB | 6 | 0 | 31-Jul-14 A | 05-Aug-14 A | |
| L08-6024 | Inspections for GWB Cover | 2 | 0 | 31-Jul-14 A | 31-Jul-14 A | |
| L12-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L14-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L06-6000 | Tape/Finish GWB | 4 | 0 | 06-Aug-14 A | 11-Aug-14 A | |
| L09-6024 | Inspections for GWB Cover | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L07-6000 | Tape/Finish GWB | 5 | 0 | 07-Aug-14 A | 16-Aug-14 A | |
| L11-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 08-Aug-14 A | 14-Aug-14 A | |

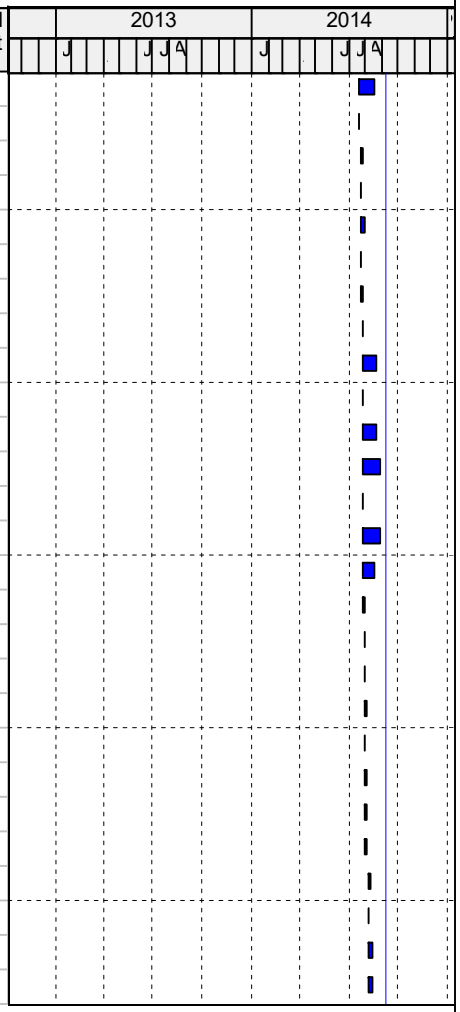



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6014 | Set Tubs & Plumbing RI | 5 | 2 | 08-Aug-14 A | 09-Sep-14 | 10 |
| L10-6024 | Inspections for GWB Cover | 2 | 0 | 11-Aug-14 A | 12-Aug-14 A | |
| L09-6000 | Tape/Finish GWB | 5 | 0 | 14-Aug-14 A | 19-Aug-14 A | |
| L08-6000 | Tape/Finish GWB | 5 | 0 | 16-Aug-14 A | 21-Aug-14 A | |
| L11-6024 | Inspections for GWB Cover | 2 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L16-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 18-Aug-14 A | 29-Aug-14 A | |
| L10-6000 | Tape/Finish GWB | 5 | 0 | 19-Aug-14 A | 23-Aug-14 A | |
| L16-6221 | Frame Unit Ceilings | 4 | 0 | 21-Aug-14 A | 26-Aug-14 A | |
| L17-6018 | HVAC RI | 3 | 1 | 21-Aug-14 A | 10-Sep-14 | 10 |
| L12-6024 | Inspections for GWB Cover | 2 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L15-6016 | Electrical RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L15-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L11-6000 | Tape/Finish GWB | 5 | 0 | 23-Aug-14 A | 29-Aug-14 A | |
| L17-6221 | Frame Unit Ceilings | 4 | 0 | 26-Aug-14 A | 28-Aug-14 A | |
| L14-6024 | Inspections for GWB Cover | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L16-6016 | Electrical RI | 5 | 2 | 28-Aug-14 A | 09-Sep-14 | 16 |
| L16-6022 | Fire Alarm / Elec Specialties RI | 5 | 2 | 28-Aug-14 A | 09-Sep-14 | 16 |
| L12-6000 | Tape/Finish GWB | 5 | 1 | 02-Sep-14 A | 08-Sep-14 | 34 |
| L15-6024 | Inspections for GWB Cover | 2 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L14-6000 | Tape/Finish GWB | 5 | 4 | 06-Sep-14 A | 11-Sep-14 | 42 |
| L17-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 1 | 08-Sep-14 | 08-Sep-14 | 10 |
| L17-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 1 | 09-Sep-14 | 09-Sep-14 | 10 |
| L17-6028 | PreRock at Heat Pumps | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 10 |
| L16-6024 | Inspections for GWB Cover | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 16 |
| L17-6029 | Inspection of PreRock at Heat Pumps | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 10 |
| L17-6030 | Tape/Firecaulk at Heat Pumps | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 10 |

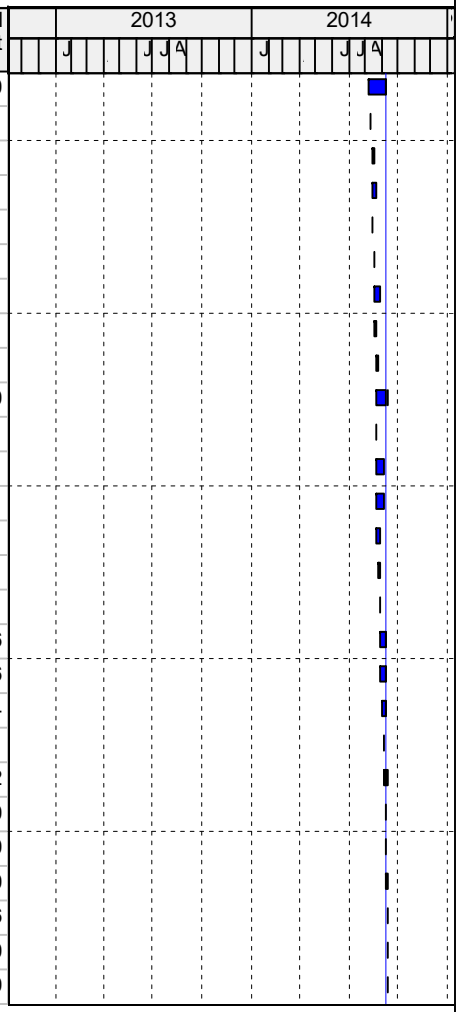



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6000 | Tape/Finish GWB | 4 | 4 | 12-Sep-14 | 16-Sep-14 | 20 |
| L17-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 1 | 12-Sep-14 | 12-Sep-14 | 10 |
| L17-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 3 | 12-Sep-14 | 16-Sep-14 | 10 |
| L17-6032 | Install Seismic Bracing at Heat Pumps | 2 | 2 | 15-Sep-14 | 16-Sep-14 | 10 |
| L17-6016 | Electrical RI | 5 | 5 | 16-Sep-14 | 22-Sep-14 | 10 |
| L17-6022 | Fire Alarm / Elec Specialties RI | 5 | 5 | 16-Sep-14 | 22-Sep-14 | 10 |
| L17-6024 | Inspections for GWB Cover | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 10 |
| L16-6000 | Tape/Finish GWB | 4 | 4 | 25-Sep-14 | 29-Sep-14 | 12 |
| L17-6000 | Tape/Finish GWB | 6 | 6 | 30-Sep-14 | 06-Oct-14 | 12 |
| **Mechanical Penthouse** | | | | | | |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 0 | 11-Jun-14 A | 20-Jun-14 A | |
| PH-6006 | PH - Exterior Wall Framing (including PH roof parapet | 6 | 0 | 12-Jun-14 A | 14-Jul-14 A | |
| PH-6014 | PH - Plumbing/Piping RI | 40 | 6 | 25-Jun-14 A | 15-Sep-14 | 7 |
| PH-6002 | PH - Layout | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| PH-6008 | PH - Interior Wall Framing | 3 | 0 | 24-Jul-14 A | 08-Aug-14 A | |
| PH-6020 | PH - H Mtl Frames | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| PH-6012 | PH - Fire Sprinkler RI | 10 | 10 | 09-Sep-14 | 22-Sep-14 | 7 |
| PH-6016 | PH - Electrical RI | 10 | 10 | 09-Sep-14 | 22-Sep-14 | 7 |
| PH-6018 | PH - HVAC RI | 10 | 10 | 09-Sep-14 | 22-Sep-14 | 7 |
| PH-6022 | PH - Fire Alarm / Elec Specialties RI | 10 | 10 | 09-Sep-14 | 22-Sep-14 | 7 |
| PH-6024 | PH - Inspections | 2 | 2 | 23-Sep-14 | 24-Sep-14 | 7 |
| **Finishes** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL4-8100 | LL4 - Insulation | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 17 |
| LL4-8102 | LL4 - GWB Hang (incl. screw inspection) | 4 | 4 | 18-Oct-14 | 22-Oct-14 | 22 |

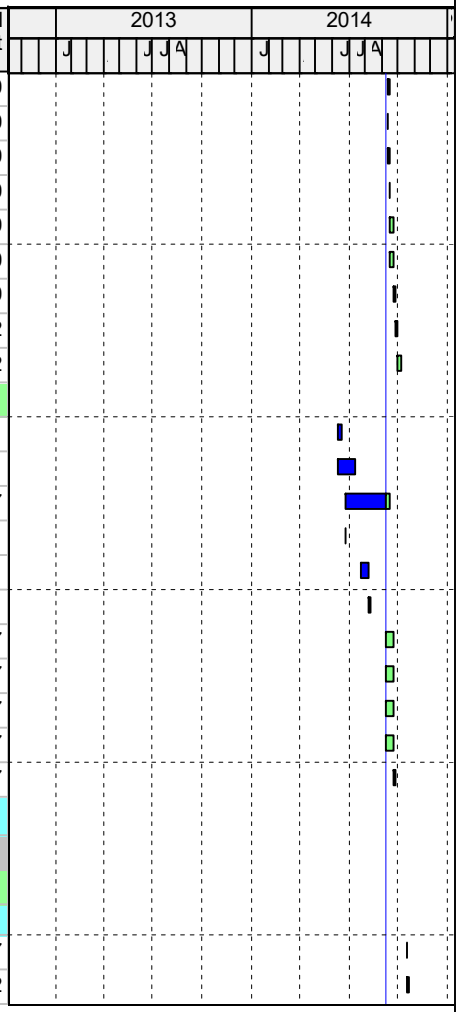



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8104 | LL4 - Int Painting | 2 | 2 | 29-Oct-14 | 30-Oct-14 | 17 |
| LL4-8122 | LL4 - Plumbing Trim / Finish | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 24 |
| LL4-8108 | LL4 - Elec Trim / Finish | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 24 |
| LL4-8110 | LL4 - HVAC Trim / Finish | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 24 |
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 25 |
| LL4-8124 | LL4 - Flooring (VCT) | 4 | 4 | 31-Oct-14 | 05-Nov-14 | 17 |
| LL4-8118 | LL4 - Elec Specialties Trim / Finish | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 25 |
| LL4-8126 | LL4 - Doors & Hardware | 3 | 3 | 04-Nov-14 | 06-Nov-14 | 17 |
| LL4-8114 | LL4 - Striping / Signage | 5 | 5 | 07-Nov-14 | 14-Nov-14 | 17 |
| LL4-8132 | LL4 - Punch | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 17 |
| LL4-8134 | LL4 - Clean | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 17 |
| LL4-8210 | LL4 - Owner Walk / Create Punchlist | 1 | 1 | 24-Nov-14 | 24-Nov-14 | 17 |
| LL4-8212 | LL4 - Resolve Final Punchlist | 5 | 5 | 25-Nov-14 | 03-Dec-14 | 17 |
| LL4-8214 | LL4 - Floor Complete | 0 | 0 | | 03-Dec-14 | 17 |
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL3-8100 | LL3 - Insulation | 3 | 3 | 16-Sep-14 | 18-Sep-14 | 36 |
| LL3-8102 | LL3 - GWB Hang (incl. screw inspection) | 4 | 4 | 17-Sep-14 | 20-Sep-14 | 36 |
| LL3-8104 | LL3 - Int Painting | 4 | 4 | 26-Sep-14 | 01-Oct-14 | 30 |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 4 | 4 | 02-Oct-14 | 07-Oct-14 | 39 |
| LL3-8108 | LL3 - Elec Trim / Finish | 4 | 4 | 02-Oct-14 | 07-Oct-14 | 39 |
| LL3-8110 | LL3 - HVAC Trim / Finish | 4 | 4 | 02-Oct-14 | 07-Oct-14 | 39 |
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 4 | 4 | 02-Oct-14 | 07-Oct-14 | 45 |
| LL3-8124 | LL3 - Flooring (VCT) | 5 | 5 | 02-Oct-14 | 08-Oct-14 | 30 |
| LL3-8118 | LL3 - Elec Specialties Trim / Finish | 4 | 4 | 02-Oct-14 | 07-Oct-14 | 45 |
| LL3-8126 | LL3 - Doors & Hardware | 3 | 3 | 09-Oct-14 | 13-Oct-14 | 30 |
| LL3-8114 | LL3 - Striping / Signage | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 30 |

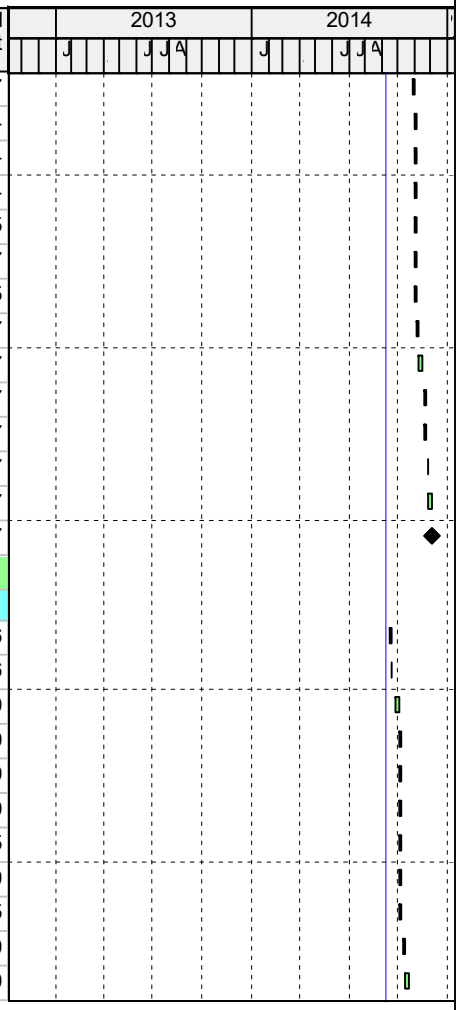



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-8132 | LL3 - Punch | 5 | 5 | 21-Oct-14 | 27-Oct-14 | 30 |
| LL3-8134 | LL3 - Clean | 5 | 5 | 21-Oct-14 | 27-Oct-14 | 30 |
| LL3-8210 | LL3 - Owner Walk / Create Punchlist | 1 | 1 | 28-Oct-14 | 28-Oct-14 | 30 |
| LL3-8212 | LL3 - Resolve Final Punchlist | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 30 |
| LL3-8214 | LL3 - Floor Complete | 0 | 0 | | 04-Nov-14 | 30 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL2E-8102 | LL2 - GWB Hang / Tape / Finish @ Electrical Rooms | 8 | 0 | 24-Jun-14 A | 03-Jul-14 A | |
| LL2-8100 | LL2 - Insulation | 5 | 5 | 18-Sep-14 | 23-Sep-14 | 42 |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish & Inspection | 6 | 6 | 19-Sep-14 | 25-Sep-14 | 44 |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 5 | 5 | 19-Sep-14 | 25-Sep-14 | 35 |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 5 | 5 | 19-Sep-14* | 25-Sep-14 | 49 |
| LL2-8104 | LL2 - Int Painting | 4 | 4 | 26-Sep-14 | 01-Oct-14 | 35 |
| LL2-8128 | LL2 - Entry Gates | 3 | 3 | 26-Sep-14 | 30-Sep-14 | 49 |
| LL2-8116 | LL2 - Finish Carpentry / Millwork | 3 | 3 | 01-Oct-14 | 03-Oct-14 | 46 |
| LL2-8122 | LL2 - Plumbing Trim / Finish | 3 | 3 | 02-Oct-14 | 06-Oct-14 | 35 |
| LL2-8108 | LL2 - Elec Trim / Finish | 3 | 3 | 02-Oct-14 | 06-Oct-14 | 35 |
| LL2-8110 | LL2 - HVAC Trim / Finish | 3 | 3 | 02-Oct-14 | 06-Oct-14 | 35 |
| LL2-8112 | LL2 - Fire Sprinkler Trim / Finish | 3 | 3 | 02-Oct-14 | 06-Oct-14 | 35 |
| LL2-8124 | LL2 - Flooring | 4 | 4 | 02-Oct-14 | 07-Oct-14 | 35 |
| LL2-8118 | LL2 - Elec Specialties Trim / Finish | 3 | 3 | 02-Oct-14 | 06-Oct-14 | 35 |
| LL2-8120 | LL2 - Install Bollards | 3 | 3 | 02-Oct-14 | 06-Oct-14 | 45 |
| LL2-8136 | LL2 - Chainlink Fencing / Gate @ Recycling | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 35 |
| LL2-8126 | LL2 - Doors & Hardware | 4 | 4 | 08-Oct-14 | 13-Oct-14 | 35 |
| LL2-8114 | LL2 - Striping / Signage | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 35 |
| LL2-8132 | LL2 - Punch | 5 | 5 | 21-Oct-14 | 27-Oct-14 | 35 |
| LL2-8134 | LL2 - Clean | 5 | 5 | 21-Oct-14 | 27-Oct-14 | 35 |

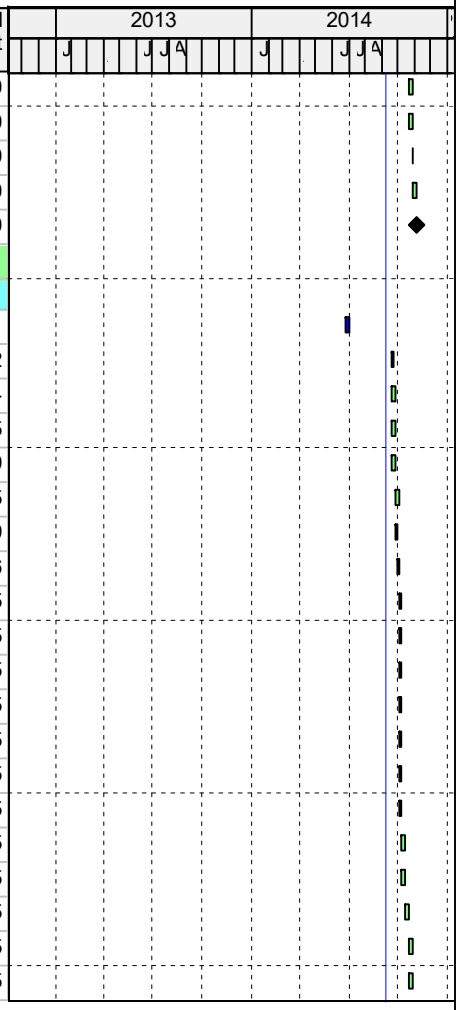



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-8210 | LL2 - Owner Walk / Create Punchlist | 1 | 1 | 28-Oct-14 | 28-Oct-14 | 35 |
| LL2-8212 | LL2 - Resolve Final Punchlist | 5 | 5 | 05-Nov-14 | 12-Nov-14 | 30 |
| LL2-8214 | LL2 - Floor Complete | 0 | 0 | | 12-Nov-14 | 30 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 31-Jul-14 A | |
| LL1-Z2U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 09-May-14 A | |
| LL1-Z3U-8102 | Above Ceiling GWB (At All Areas North of Q-Line) | 5 | 0 | 10-Feb-14 A | 20-Jun-14 A | |
| L1BU-8102 | Above Ceiling GWB [including East Service Corridor] | 5 | 0 | 06-Jun-14 A | 11-Jun-14 A | |
| L1LU-8102 | Above Ceiling GWB | 5 | 2 | 24-Jun-14 A | 10-Sep-14 | 0 |
| L1KU-8102 | Above Ceiling GWB | 2 | 0 | 26-Jun-14 A | 22-Aug-14 A | |
| LL1-8100 | Insulation | 5 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| LL1-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 28-Jul-14 A | 06-Aug-14 A | |
| LL1-Z2-8102 | GWB Hang (Walls) & Inspection | 4 | 0 | 11-Aug-14 A | 14-Aug-14 A | |
| LL1-Z2-8100 | Insulation | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| LL1-Z3-8100 | Insulation | 5 | 5 | 13-Aug-14 A | 18-Sep-14 | 15 |
| LL1-Z3-8102 | GWB Hang (Walls) & Inspection | 5 | 5 | 14-Aug-14 A | 19-Sep-14 | 15 |
| LL1-8215 | GWB Tape (Walls) | 10 | 10 | 16-Aug-14 A | 18-Sep-14 | 26 |
| L1B-8102 | GWB Hang (Walls) & Inspection | 8 | 5 | 28-Aug-14 A | 17-Sep-14 | 3 |
| L1B-8100 | Insulation | 5 | 5 | 10-Sep-14 | 16-Sep-14 | 3 |
| L1K-8100 | Insulation | 5 | 5 | 12-Sep-14 | 18-Sep-14 | 11 |
| L1K-8102 | GWB Hang (Walls) & Inspection | 8 | 8 | 13-Sep-14 | 22-Sep-14 | 14 |
| L1L-8100 | Insulation | 4 | 4 | 15-Sep-14 | 18-Sep-14 | 0 |
| L1L-8102 | GWB Hang (Walls) | 4 | 4 | 16-Sep-14 | 19-Sep-14 | 0 |
| L1B-8215 | GWB Tape (Walls) | 6 | 6 | 18-Sep-14 | 24-Sep-14 | 4 |
| L1L-8215 | GWB Tape (Walls) | 7 | 7 | 22-Sep-14 | 30-Sep-14 | 0 |
| L1K-8215 | GWB Tape (Walls & Ceilings) | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 12 |

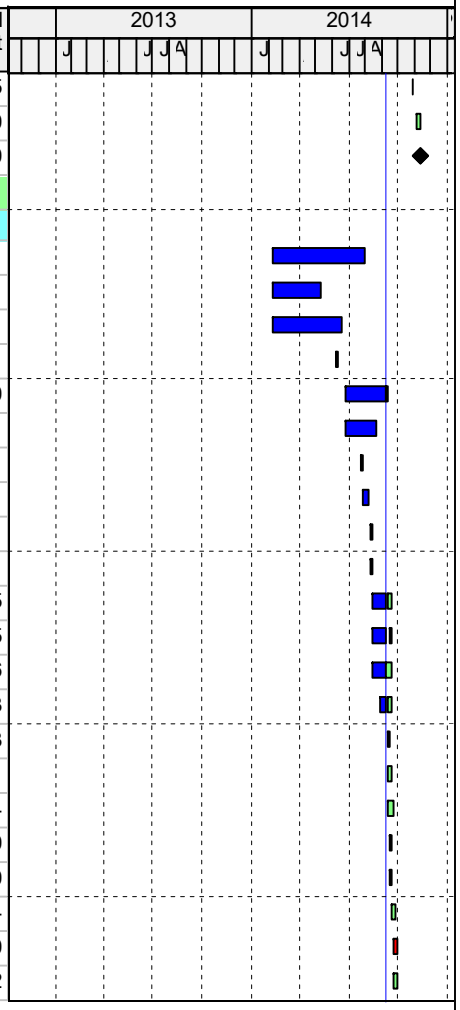



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-8215 | GWB Tape (Walls/Ceilings) | 7 | 7 | 26-Sep-14 | 06-Oct-14 | 19 |
| LL1-Z3-8215 | GWB Tape (Walls & Ceilings) | 7 | 7 | 29-Sep-14 | 07-Oct-14 | 15 |
| L1K-8104 | Prime Paint | 4 | 4 | 30-Sep-14 | 03-Oct-14 | 12 |
| L1K-8106 | Wallcoverings (FRP) | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 12 |
| L1K-8114 | T Bar Grid Ceiling | 4 | 4 | 06-Oct-14 | 09-Oct-14 | 20 |
| LL1-Z2-8104 | Prime Paint | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 19 |
| LL1-8104 | Prime Paint | 3 | 3 | 08-Oct-14 | 10-Oct-14 | 17 |
| LL1-Z3-8104 | Prime Paint | 2 | 2 | 08-Oct-14 | 09-Oct-14 | 15 |
| LL1-Z2-8114 | T Bar Grid Ceiling & Inspection | 3 | 3 | 09-Oct-14 | 13-Oct-14 | 19 |
| LL1-8114 | T Bar Grid Ceiling & Inspection | 7 | 7 | 10-Oct-14 | 17-Oct-14 | 21 |
| LL1-Z3-8114 | T Bar Grid Ceiling & Inspection | 6 | 6 | 10-Oct-14 | 17-Oct-14 | 15 |
| LL1-Z2-8106 | Wallcoverings | 4 | 4 | 15-Oct-14 | 20-Oct-14 | 19 |
| L1K-8140 | Acoustical Ceiling Tile | 4 | 4 | 17-Oct-14 | 22-Oct-14 | 12 |
| LL1-Z2-8124 | Flooring | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 19 |
| L1K-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 12 |
| L1K-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 12 |
| L1K-8124 | Flooring (VCT & Tile) | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 12 |
| LL1-Z3-8140 | Acoustical Ceiling Tile | 5 | 5 | 24-Oct-14 | 30-Oct-14 | 15 |
| LL1-8124 | Flooring | 6 | 6 | 27-Oct-14 | 03-Nov-14 | 16 |
| LL1-Z2-8116 | Finish Carpentry / Millwork | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 19 |
| LL1-Z2-8126 | Doors & Hardware | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 21 |
| LL1-Z3-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 28-Oct-14 | 30-Oct-14 | 15 |
| LL1-Z3-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 28-Oct-14 | 30-Oct-14 | 15 |
| LL1-Z2-8140 | Acoustical Ceiling Tile | 3 | 3 | 29-Oct-14 | 31-Oct-14 | 19 |
| L1B-8104 | Prime Paint | 3 | 3 | 30-Oct-14 | 03-Nov-14 | 3 |
| LL1-Z2-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 31-Oct-14 | 03-Nov-14 | 20 |
| LL1-Z2-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 19 |

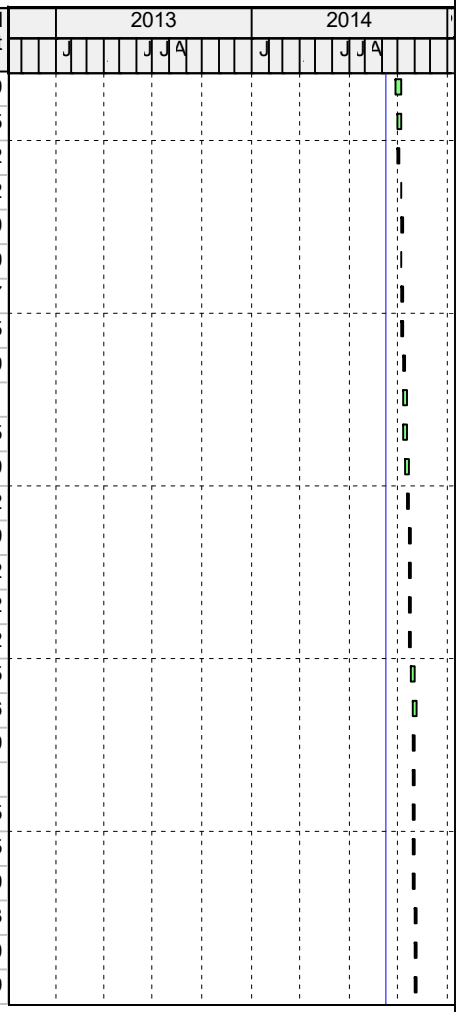



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8124 | Flooring (Epoxy) | 9 | 9 | 31-Oct-14 | 08-Nov-14 | 24 |
| LL1-8116 | Finish Carpentry / Millwork | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 16 |
| LL1-8126 | Doors & Hardware | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 16 |
| LL1-8140 | Acoustical Ceiling Tile | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 16 |
| L1K-8116 | Finish Carpentry / Millwork | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 13 |
| L1K-8126 | Doors & Hardware | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 13 |
| L1B-8114 | T Bar Grid Ceiling | 2 | 2 | 04-Nov-14 | 05-Nov-14 | 3 |
| LL1-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 16 |
| LL1-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 16 |
| L1L-8104 | Prime Paint | 3 | 3 | 07-Nov-14 | 12-Nov-14 | 0 |
| LL1-Z3-8116 | Finish Carpentry / Millwork | 4 | 4 | 11-Nov-14 | 14-Nov-14 | 15 |
| LL1-Z3-8126 | Doors & Hardware | 5 | 5 | 11-Nov-14 | 17-Nov-14 | 14 |
| LL1-Z2-8132 | Punch | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 19 |
| LL1-Z2-8134 | Clean | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 19 |
| L1L-8114 | Install wood ceiling supports | 2 | 2 | 13-Nov-14 | 14-Nov-14 | 0 |
| L1B-8124 | Flooring (Carpet) | 4 | 4 | 14-Nov-14 | 19-Nov-14 | 3 |
| L1L-8106 | Wallcoverings | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 0 |
| L1K-8132 | Punch | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 13 |
| L1K-8134 | Clean | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 13 |
| LL1-8132 | Punch | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 16 |
| LL1-8134 | Clean | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 16 |
| L1B-8116 | Finish Carpentry / Millwork | 4 | 4 | 20-Nov-14 | 25-Nov-14 | 6 |
| L1B-8126 | Doors & Hardware | 4 | 4 | 20-Nov-14 | 25-Nov-14 | 6 |
| L1B-8140 | Acoustical Ceiling Tile | 4 | 4 | 20-Nov-14 | 25-Nov-14 | 3 |
| L1L-8124 | Flooring | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 0 |
| LL1-Z3-8132 | Punch | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 14 |
| LL1-Z3-8134 | Clean | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 14 |

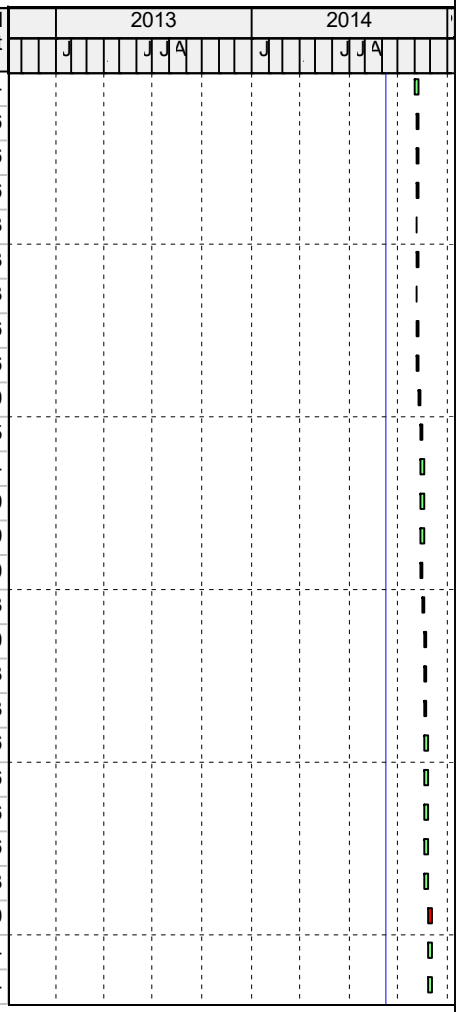



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 3 |
| L1B-8118 | Elec & Specialties Trim / Finish | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 3 |
| L1L-8140 | Install wood ceiling | 6 | 6 | 01-Dec-14 | 08-Dec-14 | 0 |
| L1L-8116 | Finish Carpentry / Millwork | 4 | 4 | 03-Dec-14 | 08-Dec-14 | 0 |
| L1L-8126 | Doors & Hardware | 4 | 4 | 03-Dec-14 | 08-Dec-14 | 0 |
| L1L-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 0 |
| L1L-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 0 |
| L1B-8132 | Punch | 4 | 4 | 10-Dec-14 | 15-Dec-14 | 3 |
| L1B-8134 | Clean | 4 | 4 | 10-Dec-14 | 15-Dec-14 | 3 |
| L1L-8132 | Punch | 4 | 4 | 16-Dec-14 | 19-Dec-14 | 0 |
| L1L-8134 | Clean | 4 | 4 | 16-Dec-14 | 19-Dec-14 | 0 |
| **Corridors / Common / Public Areas** | | | | | | |
| L1K-8200 | First Coat Finish Paint | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 12 |
| LL1-Z2-8200 | First Coat Finish Paint | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 19 |
| LL1-Z3-8200 | First Coat Finish Paint | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 15 |
| LL1-8200 | First Coat Finish Paint | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 16 |
| L1K-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 12 |
| LL1-Z3-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 28-Oct-14 | 30-Oct-14 | 15 |
| LL1-Z2-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 19 |
| LL1-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 16 |
| LL1-Z2-8201 | Final Coat Finish Paint | 5 | 5 | 05-Nov-14 | 12-Nov-14 | 19 |
| L1B-8200 | First Coat Finish Paint | 5 | 5 | 06-Nov-14 | 13-Nov-14 | 3 |
| LL1-8201 | Final Coat Finish Paint | 5 | 5 | 11-Nov-14 | 17-Nov-14 | 16 |
| L1K-8201 | Final Coat Finish Paint | 4 | 4 | 11-Nov-14 | 14-Nov-14 | 13 |
| L1L-8200 | First Coat Finish Paint | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 0 |
| LL1-Z3-8201 | Final Coat Finish Paint | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 14 |
| LL1-Z2-8210 | Owner Walk / Create Punchlist | 1 | 1 | 20-Nov-14 | 20-Nov-14 | 19 |

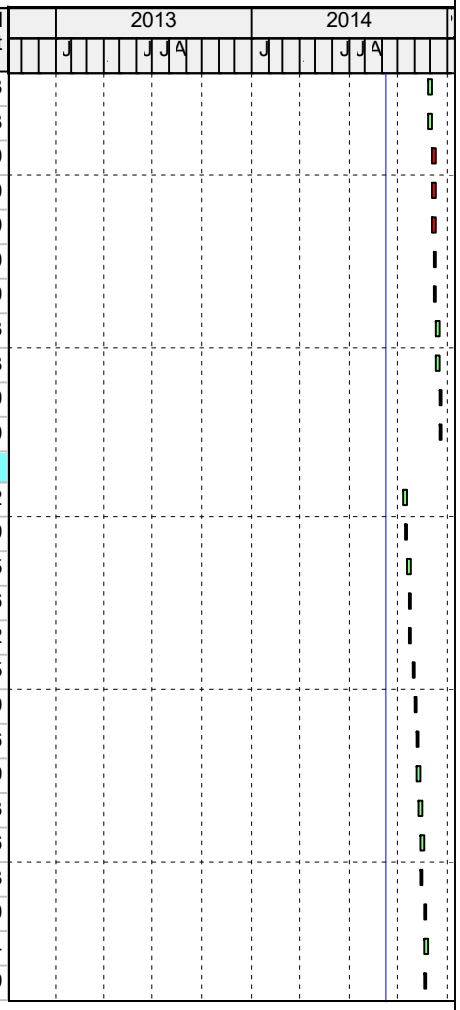



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-8212 | Resolve Final Punchlist | 5 | 5 | 21-Nov-14 | 01-Dec-14 | 19 |
| L1K-8210 | Owner Walk / Create Punchlist | 1 | 1 | 24-Nov-14 | 24-Nov-14 | 18 |
| LL1-8210 | Owner Walk / Create Punchlist | 1 | 1 | 25-Nov-14 | 25-Nov-14 | 16 |
| L1B-8204 | Mech Trim / Finish (HVAC & Plumbing) | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 3 |
| L1K-8212 | Resolve Final Punchlist | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 18 |
| LL1-8212 | Resolve Final Punchlist | 5 | 5 | 26-Nov-14 | 04-Dec-14 | 16 |
| LL1-Z2-8214 | LL1 Zone 2 Compllete | 0 | 0 | | 01-Dec-14 | 19 |
| LL1-Z3-8210 | Owner Walk / Create Punchlist | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 14 |
| L1B-8201 | Final Coat Finish Paint | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 3 |
| LL1-Z3-8212 | Resolve Final Punchlist | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 14 |
| LL1-8214 | LL1, Zone 1 Complete | 0 | 0 | | 04-Dec-14 | 16 |
| L1L-8204 | Mech Trim / Finish (HVAC & Plumbing) | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 0 |
| LL1-Z3-8214 | LL1, Zone 3 Complete | 0 | 0 | | 08-Dec-14 | 14 |
| L1L-8201 | Final Coat Finish Paint | 5 | 5 | 09-Dec-14 | 15-Dec-14 | 0 |
| L1K-8214 | L1, Zone 1 Complete | 0 | 0 | | 09-Dec-14 | 13 |
| L1B-8210 | Owner Walk / Create Punchlist | 1 | 1 | 16-Dec-14 | 16-Dec-14 | 3 |
| L1B-8212 | Resolve Final Punchlist | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 3 |
| L1L-8210 | Owner Walk / Create Punchlist | 1 | 1 | 22-Dec-14 | 22-Dec-14 | 0 |
| L1L-8212 | Resolve Final Punchlist | 4 | 4 | 23-Dec-14 | 30-Dec-14 | 0 |
| L1B-8214 | L1, Zone 2 Complete | 0 | 0 | | 23-Dec-14 | 3 |
| L1L-8214 | L1, Zone 4 Complete | 0 | 0 | | 30-Dec-14 | 0 |
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8102 | L2 - GWB Hang / Tape / Finish - (Including Common / | 10 | 10 | 25-Sep-14 | 06-Oct-14 | 33 |
| L02-8100 | L2 - Insulation | 4 | 4 | 25-Sep-14 | 30-Sep-14 | 27 |
| L02-8104 | L2 - Int Painting | 5 | 5 | 07-Oct-14 | 11-Oct-14 | 33 |
| L02-8106 | L2 - Wallcoverings | 4 | 4 | 07-Oct-14 | 10-Oct-14 | 27 |

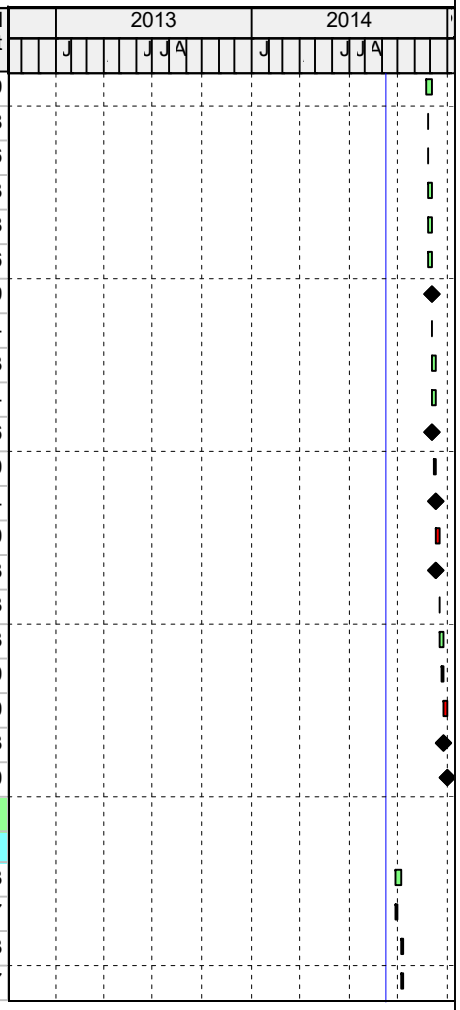



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8108 | L2 - Elec Trim / Finish | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 31 |
| L02-8110 | L2 - HVAC Trim / Finish | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 31 |
| L02-8112 | L2 - Fire Sprinkler Trim / Finish | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 31 |
| L02-8124 | L2 - Flooring | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 27 |
| L02-8118 | L2 - Elec Specialties Trim / Finish | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 31 |
| L02-8116 | L2 - Finish Carpentry / Millwork | 4 | 4 | 17-Oct-14 | 22-Oct-14 | 27 |
| L02-8120 | L2 - Ceramic Tile / Counter Tops | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 30 |
| L02-8126 | L2 - Doors & Hardware | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 27 |
| L02-8128 | L2 - Bath Specialties | 4 | 4 | 17-Oct-14 | 22-Oct-14 | 28 |
| L02-8136 | L2 - Lockers / Benches @ Locker Rooms | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 27 |
| L02-8122 | L2 - Plumbing Trim / Finish | 5 | 5 | 21-Oct-14 | 27-Oct-14 | 30 |
| L02-8132 | L2 - Punch | 5 | 5 | 31-Oct-14 | 06-Nov-14 | 27 |
| L02-8134 | L2 - Clean | 5 | 5 | 31-Oct-14 | 06-Nov-14 | 27 |
| **Corridors** | | | | | | |
| L02-8200 | L2 - Final Paint @ Common / Public Areas | 5 | 5 | 24-Oct-14 | 30-Oct-14 | 27 |
| L02-8114 | L2 - Signage | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 29 |
| L02-8210 | L2 - Owner Walk / Create Punchlist | 1 | 1 | 07-Nov-14 | 07-Nov-14 | 27 |
| L02-8212 | L2 - Resolve Final Punchlist | 5 | 5 | 11-Nov-14 | 17-Nov-14 | 27 |
| L02-8214 | L2 - Floor Complete | 0 | 0 | | 17-Nov-14 | 27 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L05-8104 | Paint (Prime) | 2 | 0 | 06-Aug-11 A | 08-Aug-14 A | |
| L03-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L04-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L05-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L06-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |

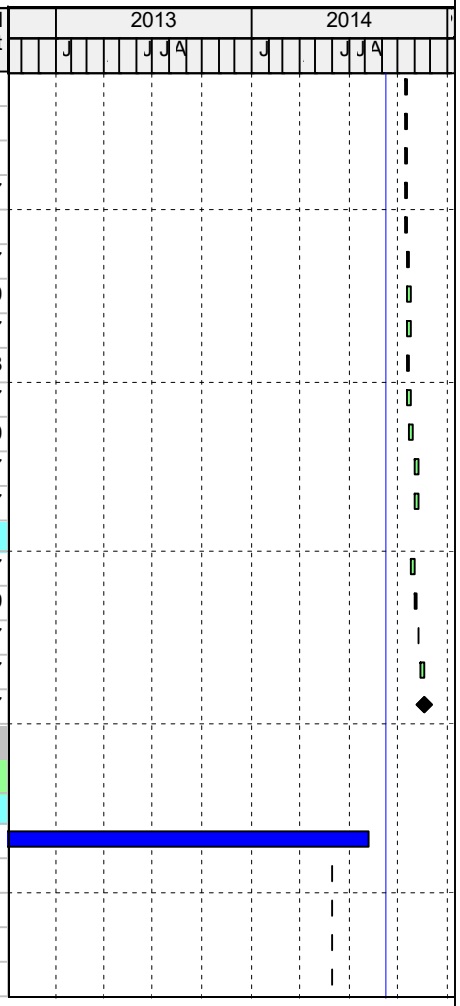


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L08-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L09-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L10-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L11-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L12-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L14-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L15-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L16-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L17-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L03-8102S | Stock GWB | 2 | 0 | 27-Jun-14 A | 08-Jul-14 A | |
| L04-8102 | Hang GWB & Inspection | 4 | 0 | 07-Jul-14 A | 16-Jul-14 A | |
| L04-8102S | Stock GWB | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-8102 | Hang GWB & Inspection | 5 | 0 | 09-Jul-14 A | 22-Jul-14 A | |
| L05-8102S | Stock GWB | 2 | 0 | 10-Jul-14 A | 14-Jul-14 A | |
| L05-8102 | Hang GWB & Inspection | 4 | 0 | 17-Jul-14 A | 23-Jul-14 A | |
| L06-8102S | Stock GWB | 2 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L04-8104 | Paint (Prime) | 2 | 0 | 28-Jul-14 A | 05-Aug-14 A | |
| L03-8104 | Paint (Prime) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L03-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L07-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L08-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L06-8102 | Hang GWB & Inspection | 5 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L07-8102 | Hang GWB & Inspection | 6 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L04-8105 | Paint (First Coat & Ceilings) | 5 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L09-8102S | Stock GWB | 2 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 07-Aug-14 A | 11-Aug-14 A | |

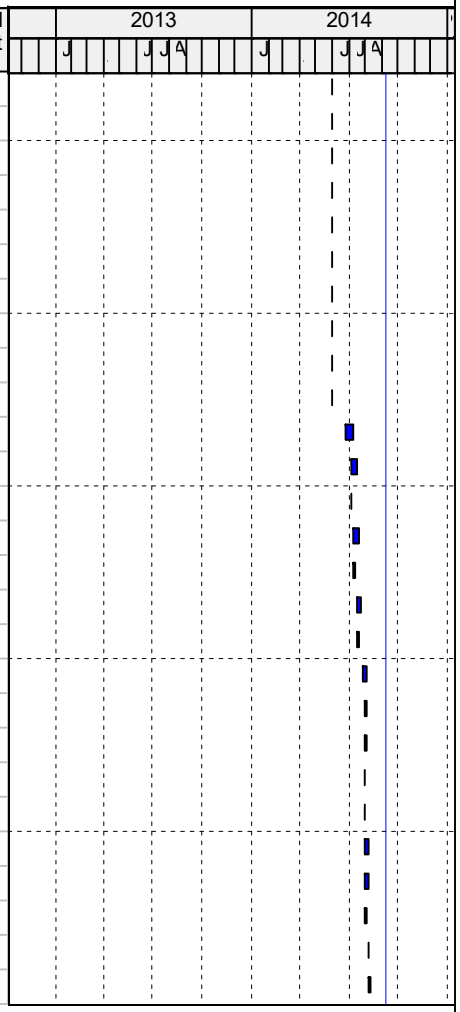



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8102 | Hang GWB & Inspection | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| L08-8102 | Hang GWB & Inspection | 6 | 0 | 11-Aug-14 A | 15-Aug-14 A | |
| L06-8104 | Paint (Prime) | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L10-8102S | Stock GWB | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-8102 | Hang GWB & Inspection | 4 | 0 | 13-Aug-14 A | 18-Aug-14 A | |
| L06-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 14-Aug-14 A | 18-Aug-14 A | |
| L11-8102S | Stock GWB | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L07-8104 | Paint (Prime) | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L11-8102 | Hang GWB & Inspection | 4 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| L07-8105 | Paint (First Coat & Ceilings) | 4 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L09-8104 | Paint (Prime) | 2 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L08-8104 | Paint (Prime) | 2 | 0 | 22-Aug-14 A | 25-Aug-14 A | |
| L12-8102 | Hang GWB & Inspection | 4 | 0 | 22-Aug-14 A | 30-Aug-14 A | |
| L12-8102S | Stock GWB | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8108 | Elec Trim / Finish | 4 | 0 | 25-Aug-14 A | 04-Sep-14 A | |
| L08-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L03-8118 | Low Voltage Trim / Finish | 5 | 4 | 27-Aug-14 A | 11-Sep-14 | 52 |
| L14-8102S | Stock GWB | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L09-8105 | Paint (First Coat & Ceilings) | 3 | 2 | 29-Aug-14 A | 09-Sep-14 | 30 |
| L14-8102 | Hang GWB & Inspection | 5 | 0 | 29-Aug-14 A | 05-Sep-14 A | |
| L03-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 02-Sep-14 A | 05-Sep-14 A | |
| L04-8124 | Guestroom/Bathroom Flooring | 5 | 2 | 04-Sep-14 A | 09-Sep-14 | 25 |
| L10-8104 | Paint (Prime) | 2 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| L15-8102S | Stock GWB | 1 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L15-8102 | Hang GWB & Inspection | 5 | 4 | 06-Sep-14 A | 11-Sep-14 | 16 |
| L03-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 34 |
| L03-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 43 |

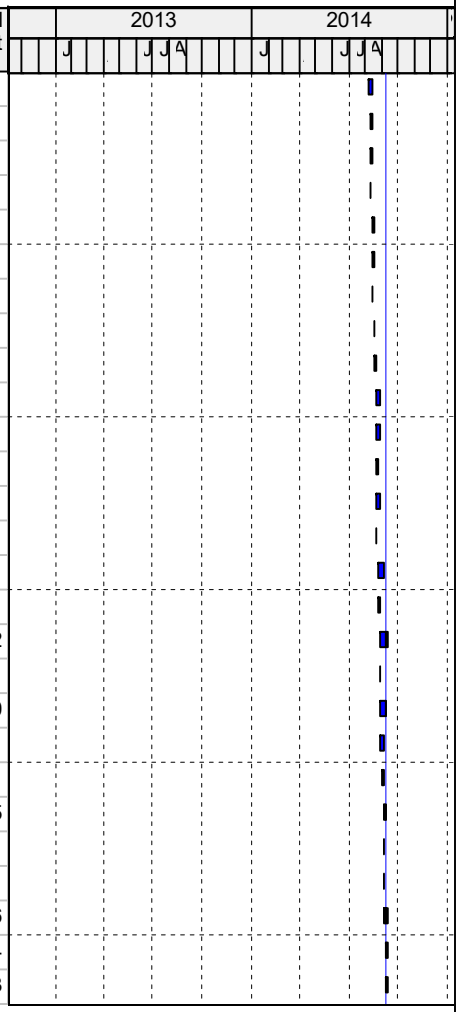


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 43 |
| L03-8128 | Install Shower/Tub Surrounds | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 16 |
| L04-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 36 |
| L04-8108 | Elec Trim / Finish | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 43 |
| L04-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 43 |
| L04-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 08-Sep-14 | 11-Sep-14 | 43 |
| L05-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 29 |
| L10-8105 | Paint (First Coat & Ceilings) | 3 | 3 | 08-Sep-14 | 10-Sep-14 | 29 |
| L11-8104 | Paint (Prime) | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 31 |
| L12-8104 | Paint (Prime) | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 34 |
| L03-8116 | Install Base at Guestrooms | 5 | 5 | 10-Sep-14 | 16-Sep-14 | 23 |
| L03-8120 | Install Countertops/Sills | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 34 |
| L03-8126 | Doors & Hardware | 5 | 5 | 10-Sep-14 | 15-Sep-14 | 25 |
| L03-8107 | Paint Final Coat | 3 | 3 | 10-Sep-14 | 12-Sep-14 | 52 |
| L03-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 53 |
| L04-8118 | Low Voltage Trim / Finish | 4 | 4 | 10-Sep-14 | 15-Sep-14 | 47 |
| L04-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 10-Sep-14 | 11-Sep-14 | 51 |
| L11-8105 | Paint (First Coat & Ceilings) | 3 | 3 | 10-Sep-14 | 12-Sep-14 | 31 |
| L04-8116 | Install Base at Guestrooms | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 22 |
| L05-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 11-Sep-14 | 12-Sep-14 | 33 |
| L12-8105 | Paint (First Coat & Ceilings) | 3 | 3 | 11-Sep-14 | 15-Sep-14 | 34 |
| L16-8102S | Stock GWB | 1 | 1 | 11-Sep-14 | 11-Sep-14 | 16 |
| L04-8120 | Install Countertops/Sills | 2 | 2 | 12-Sep-14 | 15-Sep-14 | 34 |
| L04-8128 | Install Shower/Tub Surrounds | 4 | 4 | 12-Sep-14 | 17-Sep-14 | 16 |
| L14-8104 | Paint (Prime) | 2 | 2 | 12-Sep-14 | 15-Sep-14 | 35 |
| L03-8114 | Signage (By Owner) | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 59 |
| L04-8126 | Doors & Hardware | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 25 |

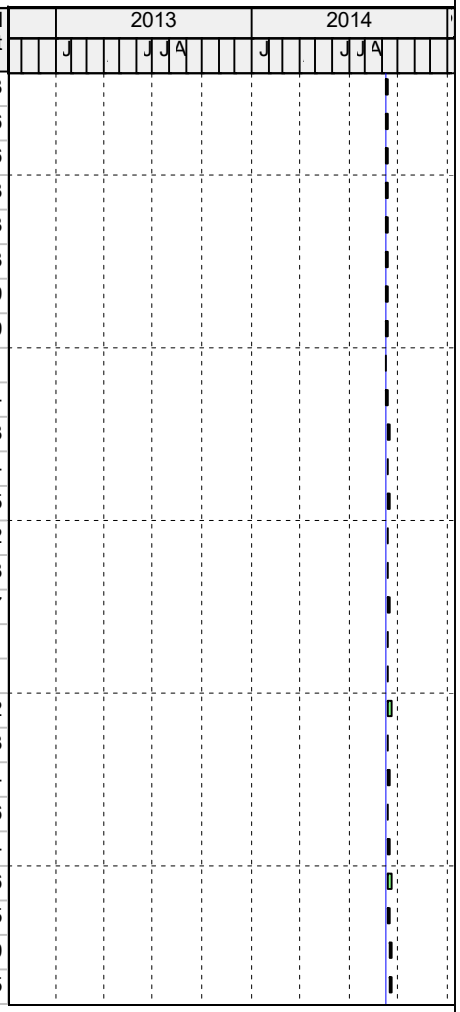



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 15-Sep-14 | 18-Sep-14 | 33 |
| L05-8108 | Elec Trim / Finish | 4 | 4 | 15-Sep-14 | 18-Sep-14 | 38 |
| L05-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 15-Sep-14 | 18-Sep-14 | 38 |
| L05-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 15-Sep-14 | 18-Sep-14 | 38 |
| L07-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 15-Sep-14 | 19-Sep-14 | 29 |
| L05-8116 | Install Base at Guestrooms | 5 | 5 | 16-Sep-14 | 22-Sep-14 | 25 |
| L06-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 16-Sep-14 | 22-Sep-14 | 22 |
| L14-8105 | Paint (First Coat & Ceilings) | 3 | 3 | 16-Sep-14 | 18-Sep-14 | 35 |
| L05-8120 | Install Countertops/Sills | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 33 |
| L05-8118 | Low Voltage Trim / Finish | 4 | 4 | 17-Sep-14 | 22-Sep-14 | 46 |
| L06-8116 | Install Base at Guestrooms | 5 | 5 | 17-Sep-14 | 23-Sep-14 | 23 |
| L15-8104 | Paint (Prime) | 2 | 2 | 17-Sep-14 | 18-Sep-14 | 23 |
| L04-8107 | Paint Final Coat | 4 | 4 | 18-Sep-14 | 23-Sep-14 | 43 |
| L05-8128 | Install Shower/Tub Surrounds | 4 | 4 | 18-Sep-14 | 22-Sep-14 | 19 |
| L06-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 18-Sep-14 | 19-Sep-14 | 30 |
| L07-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 18-Sep-14 | 19-Sep-14 | 32 |
| L08-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 18-Sep-14 | 19-Sep-14 | 34 |
| L09-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 18-Sep-14 | 19-Sep-14 | 36 |
| L10-8109 | Acoustical Ceiling Tile @ Corridors | 3 | 3 | 18-Sep-14 | 22-Sep-14 | 37 |
| L05-8126 | Doors & Hardware | 5 | 5 | 19-Sep-14 | 24-Sep-14 | 25 |
| L15-8105 | Paint (First Coat & Ceilings) | 3 | 3 | 19-Sep-14 | 23-Sep-14 | 23 |
| L16-8102 | Hang GWB & Inspection | 4 | 4 | 20-Sep-14 | 24-Sep-14 | 12 |
| L05-8107 | Paint Final Coat | 3 | 3 | 22-Sep-14 | 24-Sep-14 | 45 |
| L06-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 30 |
| L06-8108 | Elec Trim / Finish | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 38 |
| L06-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 50 |
| L06-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 50 |

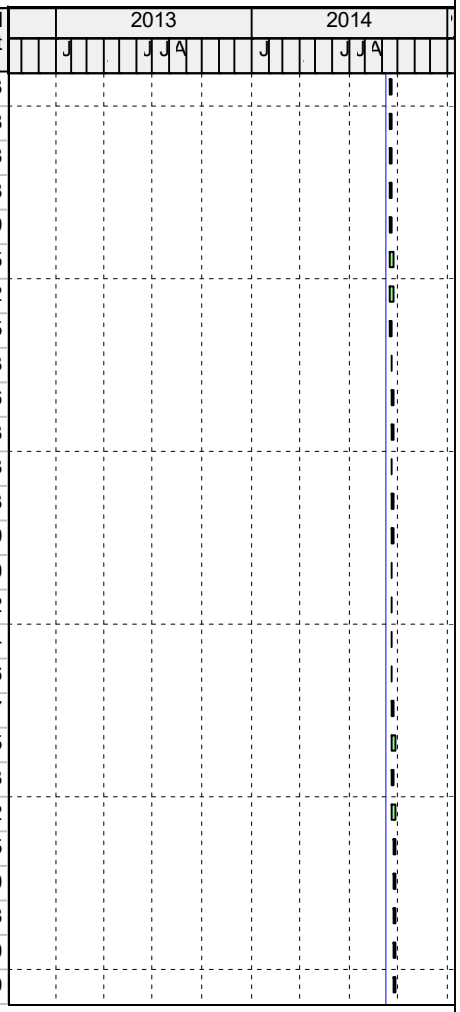



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 32 |
| L07-8108 | Elec Trim / Finish | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 38 |
| L07-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 50 |
| L07-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 50 |
| L07-8116 | Install Base at Guestrooms | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 25 |
| L08-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 34 |
| L08-8108 | Elec Trim / Finish | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 41 |
| L08-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 50 |
| L08-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 50 |
| L09-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 36 |
| L09-8108 | Elec Trim / Finish | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 44 |
| L09-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 50 |
| L09-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 22-Sep-14 | 25-Sep-14 | 50 |
| L09-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 22-Sep-14 | 26-Sep-14 | 29 |
| L11-8109 | Acoustical Ceiling Tile @ Corridors | 3 | 3 | 22-Sep-14 | 24-Sep-14 | 37 |
| L06-8128 | Install Shower/Tub Surrounds | 4 | 4 | 23-Sep-14 | 26-Sep-14 | 16 |
| L08-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 22 |
| L09-8116 | Install Base at Guestrooms | 5 | 5 | 23-Sep-14 | 29-Sep-14 | 29 |
| L10-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 23-Sep-14 | 26-Sep-14 | 37 |
| L10-8108 | Elec Trim / Finish | 4 | 4 | 23-Sep-14 | 26-Sep-14 | 42 |
| L10-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 23-Sep-14 | 26-Sep-14 | 49 |
| L10-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 23-Sep-14 | 26-Sep-14 | 49 |
| L12-8109 | Acoustical Ceiling Tile @ Corridors | 3 | 3 | 23-Sep-14 | 25-Sep-14 | 38 |
| L04-8114 | Signage (By Owner) | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 52 |
| L06-8120 | Install Countertops/Sills | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 30 |
| L06-8126 | Doors & Hardware | 5 | 5 | 24-Sep-14 | 29-Sep-14 | 25 |
| L06-8118 | Low Voltage Trim / Finish | 4 | 4 | 24-Sep-14 | 29-Sep-14 | 38 |

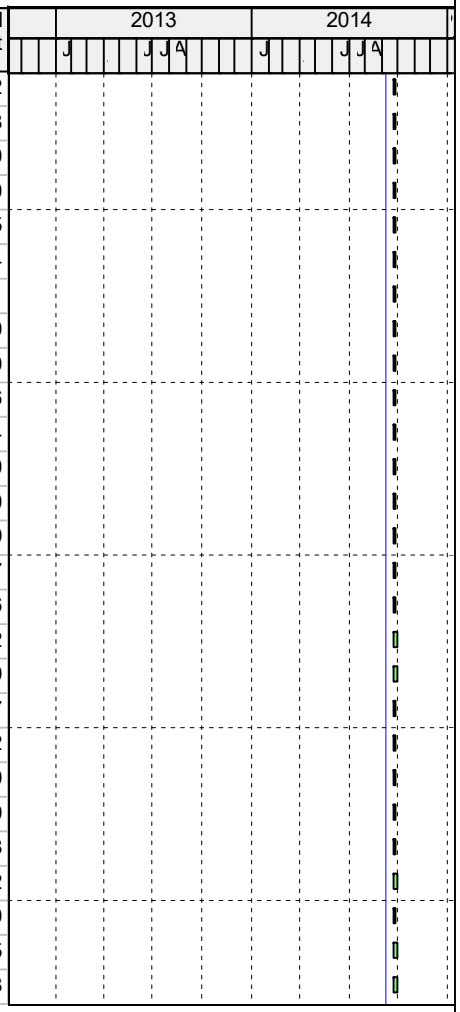


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8118 | Low Voltage Trim / Finish | 4 | 4 | 24-Sep-14 | 29-Sep-14 | 38 |
| L08-8116 | Install Base at Guestrooms | 5 | 5 | 24-Sep-14 | 30-Sep-14 | 22 |
| L08-8118 | Low Voltage Trim / Finish | 4 | 4 | 24-Sep-14 | 29-Sep-14 | 41 |
| L09-8118 | Low Voltage Trim / Finish | 4 | 4 | 24-Sep-14 | 29-Sep-14 | 44 |
| L17-8102S | Stock GWB | 1 | 1 | 24-Sep-14 | 24-Sep-14 | 10 |
| L05-8114 | Signage (By Owner) | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 51 |
| L10-8118 | Low Voltage Trim / Finish | 4 | 4 | 25-Sep-14 | 30-Sep-14 | 42 |
| L11-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 25-Sep-14 | 30-Sep-14 | 37 |
| L11-8108 | Elec Trim / Finish | 4 | 4 | 25-Sep-14 | 30-Sep-14 | 40 |
| L11-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 25-Sep-14 | 30-Sep-14 | 47 |
| L11-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 25-Sep-14 | 30-Sep-14 | 47 |
| L17-8102 | Hang GWB & Inspection | 4 | 4 | 25-Sep-14 | 29-Sep-14 | 12 |
| L07-8120 | Install Countertops/Sills | 2 | 2 | 26-Sep-14 | 29-Sep-14 | 30 |
| L12-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 26-Sep-14 | 01-Oct-14 | 38 |
| L12-8108 | Elec Trim / Finish | 4 | 4 | 26-Sep-14 | 01-Oct-14 | 39 |
| L12-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 26-Sep-14 | 01-Oct-14 | 46 |
| L12-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 26-Sep-14 | 01-Oct-14 | 46 |
| L14-8109 | Acoustical Ceiling Tile @ Corridors | 3 | 3 | 26-Sep-14 | 30-Sep-14 | 36 |
| L07-8126 | Doors & Hardware | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 25 |
| L07-8128 | Install Shower/Tub Surrounds | 4 | 4 | 29-Sep-14 | 02-Oct-14 | 16 |
| L11-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 29-Sep-14 | 03-Oct-14 | 29 |
| L11-8118 | Low Voltage Trim / Finish | 4 | 4 | 29-Sep-14 | 02-Oct-14 | 40 |
| L06-8107 | Paint Final Coat | 3 | 3 | 30-Sep-14 | 02-Oct-14 | 38 |
| L08-8120 | Install Countertops/Sills | 2 | 2 | 30-Sep-14 | 01-Oct-14 | 30 |
| L10-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 22 |
| L10-8128 | Install Shower/Tub Surrounds | 4 | 4 | 30-Sep-14 | 03-Oct-14 | 16 |
| L11-8116 | Install Base at Guestrooms | 5 | 5 | 30-Sep-14 | 06-Oct-14 | 29 |

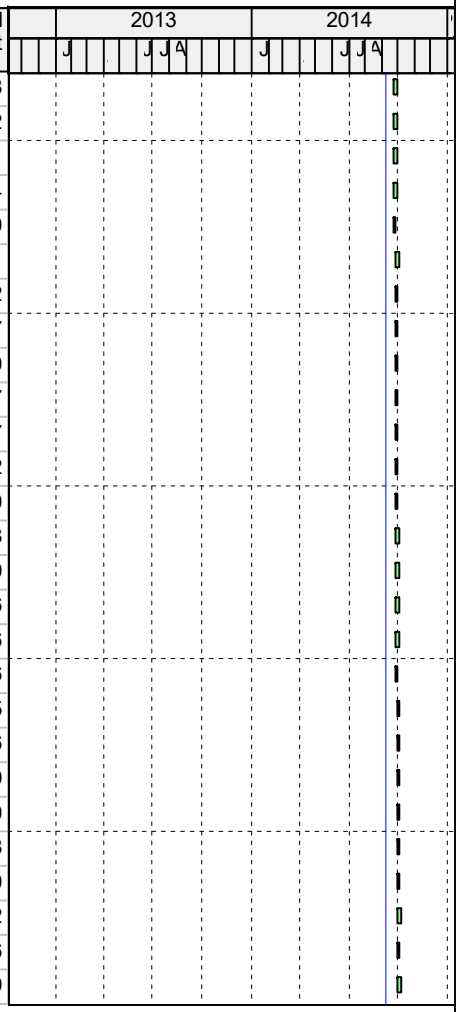



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8118 | Low Voltage Trim / Finish | 4 | 4 | 30-Sep-14 | 03-Oct-14 | 39 |
| L16-8104 | Paint (Prime) | 2 | 2 | 30-Sep-14 | 01-Oct-14 | 15 |
| L10-8116 | Install Base at Guestrooms | 5 | 5 | 01-Oct-14 | 07-Oct-14 | 22 |
| L14-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 01-Oct-14 | 06-Oct-14 | 37 |
| L14-8108 | Elec Trim / Finish | 4 | 4 | 01-Oct-14 | 06-Oct-14 | 36 |
| L14-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 01-Oct-14 | 06-Oct-14 | 43 |
| L14-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 01-Oct-14 | 06-Oct-14 | 43 |
| L15-8109 | Acoustical Ceiling Tile @ Corridors | 3 | 3 | 01-Oct-14 | 03-Oct-14 | 23 |
| L07-8107 | Paint Final Coat | 3 | 3 | 02-Oct-14 | 06-Oct-14 | 36 |
| L09-8120 | Install Countertops/Sills | 2 | 2 | 02-Oct-14 | 03-Oct-14 | 30 |
| L16-8105 | Paint (First Coat & Ceilings) | 3 | 3 | 02-Oct-14 | 06-Oct-14 | 15 |
| L06-8114 | Signage (By Owner) | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 45 |
| L08-8128 | Install Shower/Tub Surrounds | 4 | 4 | 03-Oct-14 | 08-Oct-14 | 34 |
| L14-8118 | Low Voltage Trim / Finish | 4 | 4 | 03-Oct-14 | 08-Oct-14 | 36 |
| L08-8126 | Doors & Hardware | 5 | 5 | 04-Oct-14 | 09-Oct-14 | 25 |
| L05-8132 | Punchlist @ Guestrooms | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 44 |
| L05-8134 | Final Clean @ Guestrooms | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 44 |
| L10-8120 | Install Countertops/Sills | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 30 |
| L11-8128 | Install Shower/Tub Surrounds | 4 | 4 | 06-Oct-14 | 09-Oct-14 | 16 |
| L14-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 29 |
| L15-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 06-Oct-14 | 09-Oct-14 | 36 |
| L15-8108 | Elec Trim / Finish | 4 | 4 | 06-Oct-14 | 09-Oct-14 | 23 |
| L15-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 06-Oct-14 | 09-Oct-14 | 23 |
| L15-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 06-Oct-14 | 09-Oct-14 | 23 |
| L04-8132 | Punchlist @ Guestrooms | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 43 |
| L04-8134 | Final Clean @ Guestrooms | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 43 |
| L07-8114 | Signage (By Owner) | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 38 |

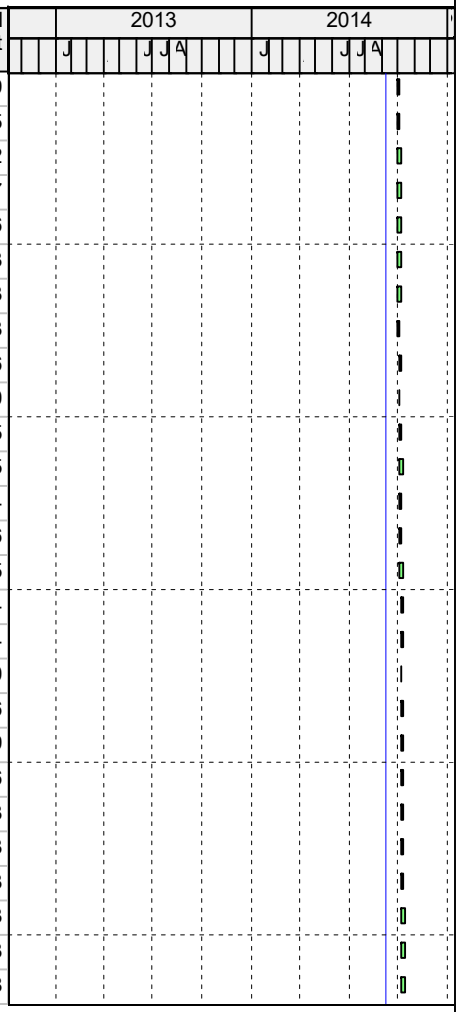



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 22 |
| L14-8116 | Install Base at Guestrooms | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 29 |
| L17-8104 | Paint (Prime) | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 10 |
| L08-8107 | Paint Final Coat | 5 | 5 | 08-Oct-14 | 14-Oct-14 | 35 |
| L11-8120 | Install Countertops/Sills | 2 | 2 | 08-Oct-14 | 09-Oct-14 | 30 |
| L12-8116 | Install Base at Guestrooms | 5 | 5 | 08-Oct-14 | 14-Oct-14 | 22 |
| L15-8118 | Low Voltage Trim / Finish | 4 | 4 | 08-Oct-14 | 13-Oct-14 | 33 |
| L09-8126 | Doors & Hardware | 5 | 5 | 09-Oct-14 | 14-Oct-14 | 25 |
| L09-8128 | Install Shower/Tub Surrounds | 4 | 4 | 09-Oct-14 | 14-Oct-14 | 34 |
| L17-8105 | Paint (First Coat & Ceilings) | 3 | 3 | 09-Oct-14 | 13-Oct-14 | 10 |
| L12-8120 | Install Countertops/Sills | 2 | 2 | 10-Oct-14 | 13-Oct-14 | 30 |
| L12-8128 | Install Shower/Tub Surrounds | 4 | 4 | 10-Oct-14 | 15-Oct-14 | 16 |
| L16-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 29 |
| L06-8132 | Punchlist @ Guestrooms | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 38 |
| L06-8134 | Final Clean @ Guestrooms | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 38 |
| L09-8107 | Paint Final Coat | 3 | 3 | 14-Oct-14 | 16-Oct-14 | 34 |
| L10-8126 | Doors & Hardware | 5 | 5 | 14-Oct-14 | 18-Oct-14 | 25 |
| L14-8120 | Install Countertops/Sills | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 30 |
| L15-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 22 |
| L16-8116 | Install Base at Guestrooms | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 29 |
| L16-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 15 |
| L08-8114 | Signage (By Owner) | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 37 |
| L15-8116 | Install Base at Guestrooms | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 22 |
| L07-8132 | Punchlist @ Guestrooms | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 36 |
| L07-8134 | Final Clean @ Guestrooms | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 36 |
| L14-8128 | Install Shower/Tub Surrounds | 4 | 4 | 16-Oct-14 | 21-Oct-14 | 16 |
| L15-8120 | Install Countertops/Sills | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 30 |

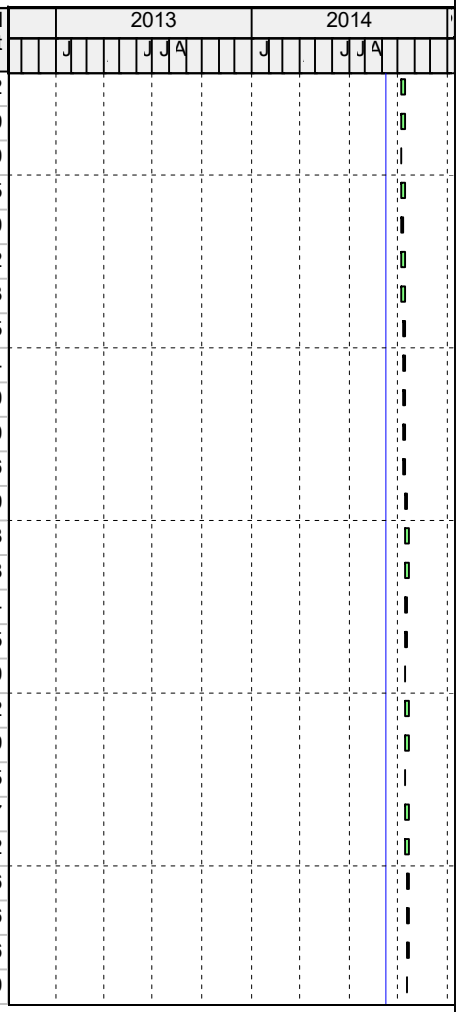



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 16-Oct-14 | 21-Oct-14 | 30 |
| L16-8108 | Elec Trim / Finish | 4 | 4 | 16-Oct-14 | 21-Oct-14 | 15 |
| L16-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 16-Oct-14 | 21-Oct-14 | 33 |
| L16-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 16-Oct-14 | 21-Oct-14 | 15 |
| L08-8132 | Punchlist @ Guestrooms | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 35 |
| L08-8134 | Final Clean @ Guestrooms | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 35 |
| L09-8114 | Signage (By Owner) | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 35 |
| L11-8126 | Doors & Hardware | 5 | 5 | 18-Oct-14 | 23-Oct-14 | 25 |
| L09-8132 | Punchlist @ Guestrooms | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 34 |
| L09-8134 | Final Clean @ Guestrooms | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 34 |
| L10-8107 | Paint Final Coat | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 29 |
| L16-8120 | Install Countertops/Sills | 2 | 2 | 20-Oct-14 | 21-Oct-14 | 30 |
| L16-8118 | Low Voltage Trim / Finish | 4 | 4 | 20-Oct-14 | 23-Oct-14 | 23 |
| L17-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 21-Oct-14 | 27-Oct-14 | 22 |
| L17-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 21-Oct-14 | 22-Oct-14 | 10 |
| L15-8128 | Install Shower/Tub Surrounds | 4 | 4 | 22-Oct-14 | 27-Oct-14 | 16 |
| L17-8116 | Install Base at Guestrooms | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 22 |
| L10-8114 | Signage (By Owner) | 5 | 5 | 23-Oct-14 | 29-Oct-14 | 31 |
| L12-8126 | Doors & Hardware | 5 | 5 | 23-Oct-14 | 28-Oct-14 | 25 |
| L17-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 23-Oct-14 | 28-Oct-14 | 27 |
| L17-8108 | Elec Trim / Finish | 4 | 4 | 23-Oct-14 | 28-Oct-14 | 10 |
| L17-8110 | HVAC Trim / Finish (including Corridors) | 4 | 4 | 23-Oct-14 | 28-Oct-14 | 10 |
| L17-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 23-Oct-14 | 28-Oct-14 | 10 |
| L11-8107 | Paint Final Coat | 3 | 3 | 24-Oct-14 | 28-Oct-14 | 25 |
| L17-8120 | Install Countertops/Sills | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 27 |
| L17-8118 | Low Voltage Trim / Finish | 4 | 4 | 27-Oct-14 | 30-Oct-14 | 20 |
| L10-8132 | Punchlist @ Guestrooms | 5 | 5 | 27-Oct-14 | 03-Nov-14 | 29 |

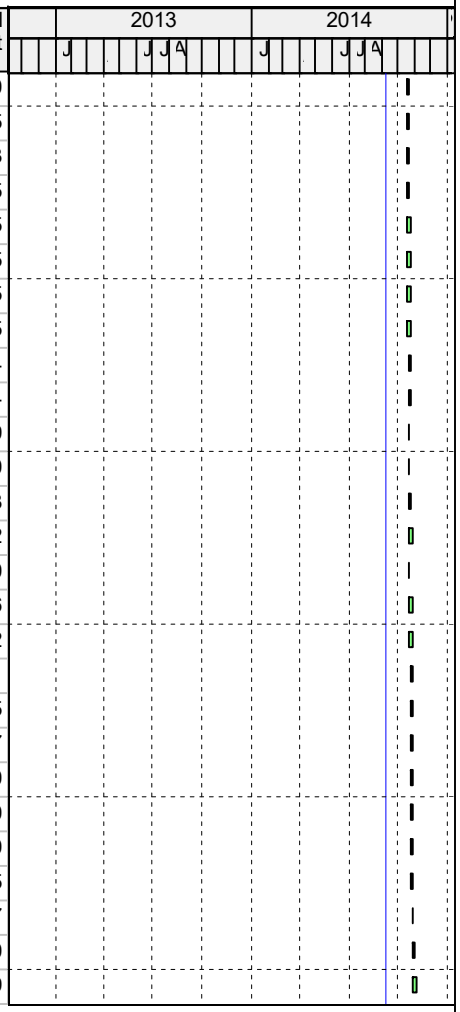



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8134 | Final Clean @ Guestrooms | 5 | 5 | 27-Oct-14 | 03-Nov-14 | 29 |
| L14-8126 | Doors & Hardware | 5 | 5 | 28-Oct-14 | 01-Nov-14 | 25 |
| L16-8128 | Install Shower/Tub Surrounds | 4 | 4 | 28-Oct-14 | 31-Oct-14 | 16 |
| L11-8114 | Signage (By Owner) | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 27 |
| L12-8107 | Paint Final Coat | 3 | 3 | 30-Oct-14 | 03-Nov-14 | 21 |
| L11-8132 | Punchlist @ Guestrooms | 5 | 5 | 31-Oct-14 | 06-Nov-14 | 25 |
| L11-8134 | Final Clean @ Guestrooms | 5 | 5 | 31-Oct-14 | 06-Nov-14 | 25 |
| L15-8126 | Doors & Hardware | 5 | 5 | 01-Nov-14 | 06-Nov-14 | 25 |
| L03-8132 | Punchlist @ Guestrooms | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 24 |
| L03-8134 | Final Clean @ Guestrooms | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 24 |
| L14-8107 | Paint Final Coat | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 19 |
| L17-8128 | Install Shower/Tub Surrounds | 4 | 4 | 03-Nov-14 | 06-Nov-14 | 16 |
| L12-8114 | Signage (By Owner) | 5 | 5 | 04-Nov-14 | 11-Nov-14 | 23 |
| L12-8132 | Punchlist @ Guestrooms | 5 | 5 | 05-Nov-14 | 12-Nov-14 | 22 |
| L12-8134 | Final Clean @ Guestrooms | 5 | 5 | 05-Nov-14 | 12-Nov-14 | 22 |
| L14-8114 | Signage (By Owner) | 5 | 5 | 06-Nov-14 | 13-Nov-14 | 21 |
| L16-8126 | Doors & Hardware | 5 | 5 | 06-Nov-14 | 11-Nov-14 | 25 |
| L14-8132 | Punchlist @ Guestrooms | 5 | 5 | 07-Nov-14 | 14-Nov-14 | 20 |
| L14-8134 | Final Clean @ Guestrooms | 5 | 5 | 07-Nov-14 | 14-Nov-14 | 20 |
| L15-8107 | Paint Final Coat | 3 | 3 | 07-Nov-14 | 12-Nov-14 | 15 |
| L17-8126 | Doors & Hardware | 5 | 5 | 11-Nov-14 | 15-Nov-14 | 25 |
| L15-8114 | Signage (By Owner) | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 17 |
| L16-8107 | Paint Final Coat | 3 | 3 | 13-Nov-14 | 17-Nov-14 | 10 |
| L15-8132 | Punchlist @ Guestrooms | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 15 |
| L15-8134 | Final Clean @ Guestrooms | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 15 |
| L17-8107 | Paint Final Coat | 3 | 3 | 17-Nov-14 | 19-Nov-14 | 10 |
| L16-8114 | Signage (By Owner) | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 14 |

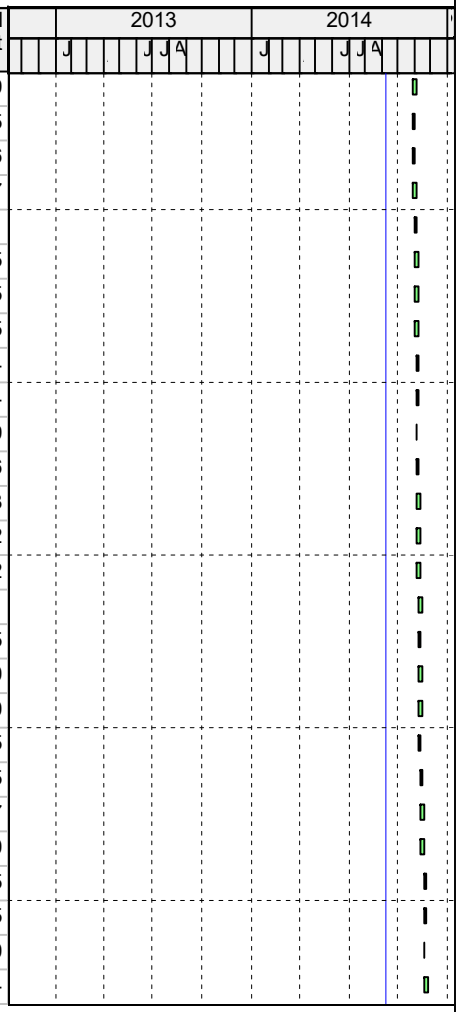



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8114 | Signage (By Owner) | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 12 |
| L16-8132 | Punchlist @ Guestrooms | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 12 |
| L16-8134 | Final Clean @ Guestrooms | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 12 |
| L17-8132 | Punchlist @ Guestrooms | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 10 |
| L17-8134 | Final Clean @ Guestrooms | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 10 |
| **Pool Area** | | | | | | |
| L03-8216 | Pool - Install tile, coping and depth markers | 10 | 10 | 26-Sep-14 | 09-Oct-14 | 12 |
| L03-8218 | Pool - Install pool equipment | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 12 |
| **Corridors / Common / Public Areas** | | | | | | |
| L03-8200 | Vinyl Wall Coverings | 3 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L04-8200 | Vinyl Wall Coverings | 5 | 0 | 06-Aug-14 A | 12-Aug-14 A | |
| L05-8200 | Vinyl Wall Coverings | 5 | 1 | 12-Aug-14 A | 08-Sep-14 | 33 |
| L03-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 53 |
| L04-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 08-Sep-14 | 09-Sep-14 | 51 |
| L06-8200 | Vinyl Wall Coverings | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 30 |
| L07-8200 | Vinyl Wall Coverings | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 32 |
| L08-8200 | Vinyl Wall Coverings | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 34 |
| L09-8200 | Vinyl Wall Coverings | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 36 |
| L10-8200 | Vinyl Wall Coverings | 5 | 5 | 08-Sep-14 | 12-Sep-14 | 37 |
| L05-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 09-Sep-14 | 10-Sep-14 | 33 |
| L11-8200 | Vinyl Wall Coverings | 5 | 5 | 10-Sep-14 | 16-Sep-14 | 37 |
| L12-8200 | Vinyl Wall Coverings | 5 | 5 | 11-Sep-14 | 17-Sep-14 | 38 |
| L06-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 30 |
| L07-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 32 |
| L08-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 34 |
| L09-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 36 |
| L10-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 16-Sep-14 | 17-Sep-14 | 37 |

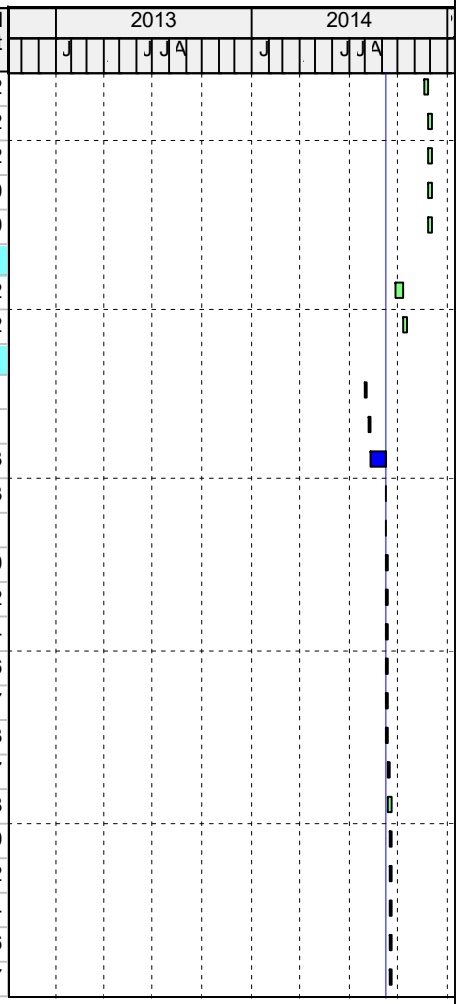



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8200 | Vinyl Wall Coverings | 5 | 5 | 16-Sep-14 | 22-Sep-14 | 36 |
| L11-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 18-Sep-14 | 19-Sep-14 | 37 |
| L12-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 19-Sep-14 | 22-Sep-14 | 38 |
| L15-8200 | Vinyl Wall Coverings | 5 | 5 | 19-Sep-14 | 25-Sep-14 | 23 |
| L04-8206 | Install Flooring @ Corridors | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 43 |
| L14-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 24-Sep-14 | 25-Sep-14 | 36 |
| L05-8206 | Install Flooring @ Corridors | 5 | 5 | 25-Sep-14 | 01-Oct-14 | 45 |
| L15-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 29-Sep-14 | 30-Sep-14 | 23 |
| L16-8200 | Vinyl Wall Coverings | 5 | 5 | 02-Oct-14 | 08-Oct-14 | 15 |
| L06-8206 | Install Flooring @ Corridors | 5 | 5 | 03-Oct-14 | 09-Oct-14 | 38 |
| L07-8206 | Install Flooring @ Corridors | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 36 |
| L17-8200 | Vinyl Wall Coverings | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 10 |
| L16-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 10-Oct-14 | 13-Oct-14 | 15 |
| L05-8208 | Final Clean (Entire Floor) | 2 | 2 | 13-Oct-14 | 14-Oct-14 | 44 |
| L04-8208 | Final Clean (Entire Floor) | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 43 |
| L05-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 15-Oct-14 | 15-Oct-14 | 44 |
| L08-8206 | Install Flooring @ Corridors | 2 | 2 | 15-Oct-14 | 16-Oct-14 | 35 |
| L04-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 16-Oct-14 | 16-Oct-14 | 43 |
| L05-8212 | Resolve Final Punchlist | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 44 |
| L04-8212 | Resolve Final Punchlist | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 43 |
| L09-8206 | Install Flooring @ Corridors | 2 | 2 | 17-Oct-14 | 20-Oct-14 | 34 |
| L17-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 17-Oct-14 | 20-Oct-14 | 10 |
| L06-8208 | Final Clean (Entire Floor) | 2 | 2 | 21-Oct-14 | 22-Oct-14 | 38 |
| L05-8214 | Floor Complete | 0 | 0 | | 22-Oct-14 | 44 |
| L06-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 23-Oct-14 | 23-Oct-14 | 38 |
| L07-8208 | Final Clean (Entire Floor) | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 36 |
| L10-8206 | Install Flooring @ Corridors | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 29 |

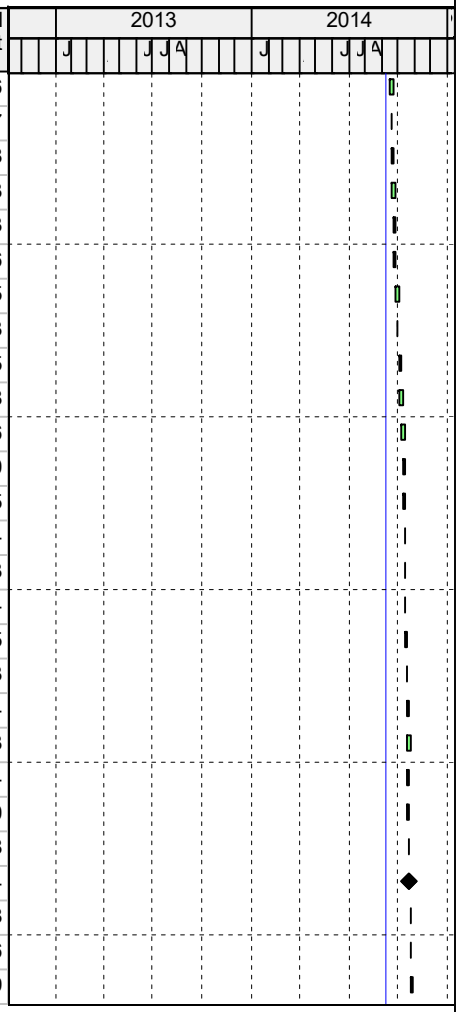



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8214 | Floor Complete | 0 | 0 | | 23-Oct-14 | 43 |
| L03-8206 | Install Flooring @ Corridors | 4 | 4 | 24-Oct-14 | 28-Oct-14 | 29 |
| L06-8212 | Resolve Final Punchlist | 5 | 5 | 24-Oct-14 | 30-Oct-14 | 38 |
| L08-8208 | Final Clean (Entire Floor) | 2 | 2 | 24-Oct-14 | 27-Oct-14 | 35 |
| L07-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 27-Oct-14 | 27-Oct-14 | 36 |
| L09-8208 | Final Clean (Entire Floor) | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 34 |
| L07-8212 | Resolve Final Punchlist | 5 | 5 | 28-Oct-14 | 03-Nov-14 | 36 |
| L08-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 28-Oct-14 | 28-Oct-14 | 35 |
| L08-8212 | Resolve Final Punchlist | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 35 |
| L09-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 34 |
| L11-8206 | Install Flooring @ Corridors | 3 | 3 | 29-Oct-14 | 31-Oct-14 | 25 |
| L09-8212 | Resolve Final Punchlist | 5 | 5 | 30-Oct-14 | 05-Nov-14 | 34 |
| L06-8214 | Floor Complete | 0 | 0 | | 30-Oct-14 | 38 |
| L10-8208 | Final Clean (Entire Floor) | 2 | 2 | 03-Nov-14 | 05-Nov-14 | 29 |
| L07-8214 | Floor Complete | 0 | 0 | | 03-Nov-14 | 36 |
| L12-8206 | Install Flooring @ Corridors | 4 | 4 | 04-Nov-14 | 07-Nov-14 | 26 |
| L08-8214 | Floor Complete | 0 | 0 | | 04-Nov-14 | 35 |
| L10-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 05-Nov-14 | 06-Nov-14 | 29 |
| L09-8214 | Floor Complete | 0 | 0 | | 05-Nov-14 | 34 |
| L14-8206 | Install Flooring @ Corridors | 4 | 4 | 06-Nov-14 | 10-Nov-14 | 24 |
| L10-8212 | Resolve Final Punchlist | 5 | 5 | 06-Nov-14 | 14-Nov-14 | 29 |
| L11-8208 | Final Clean (Entire Floor) | 2 | 2 | 07-Nov-14 | 11-Nov-14 | 25 |
| L11-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 12-Nov-14 | 12-Nov-14 | 25 |
| L11-8212 | Resolve Final Punchlist | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 25 |
| L12-8208 | Final Clean (Entire Floor) | 2 | 2 | 13-Nov-14 | 14-Nov-14 | 22 |
| L15-8206 | Install Flooring @ Corridors | 4 | 4 | 13-Nov-14 | 17-Nov-14 | 18 |
| L10-8214 | Floor Complete | 0 | 0 | | 14-Nov-14 | 29 |

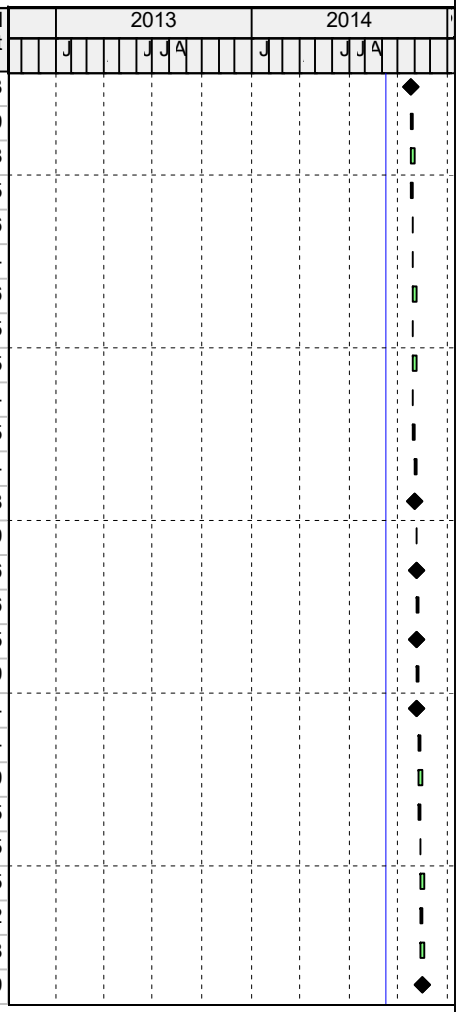



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 17-Nov-14 | 17-Nov-14 | 22 |
| L14-8208 | Final Clean (Entire Floor) | 2 | 2 | 17-Nov-14 | 18-Nov-14 | 20 |
| L12-8212 | Resolve Final Punchlist | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 22 |
| L16-8206 | Install Flooring @ Corridors | 2 | 2 | 18-Nov-14 | 19-Nov-14 | 10 |
| L14-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 19-Nov-14 | 19-Nov-14 | 20 |
| L11-8214 | Floor Complete | 0 | 0 | | 19-Nov-14 | 25 |
| L14-8212 | Resolve Final Punchlist | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 20 |
| L17-8206 | Install Flooring @ Corridors | 4 | 4 | 20-Nov-14 | 24-Nov-14 | 12 |
| L15-8208 | Final Clean (Entire Floor) | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 15 |
| L12-8214 | Floor Complete | 0 | 0 | | 24-Nov-14 | 22 |
| L15-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 26-Nov-14 | 26-Nov-14 | 15 |
| L14-8214 | Floor Complete | 0 | 0 | | 26-Nov-14 | 20 |
| L03-8208 | Final Clean (Entire Floor) | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 12 |
| L15-8212 | Resolve Final Punchlist | 5 | 5 | 01-Dec-14 | 05-Dec-14 | 15 |
| L03-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 12 |
| L16-8208 | Final Clean (Entire Floor) | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 10 |
| L17-8208 | Final Clean (Entire Floor) | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 10 |
| L03-8212 | Resolve Final Punchlist | 5 | 5 | 04-Dec-14 | 10-Dec-14 | 12 |
| L16-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 05-Dec-14 | 05-Dec-14 | 10 |
| L17-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 05-Dec-14 | 05-Dec-14 | 10 |
| L15-8214 | Floor Complete | 0 | 0 | | 05-Dec-14 | 15 |
| L16-8212 | Resolve Final Punchlist | 5 | 5 | 08-Dec-14 | 12-Dec-14 | 10 |
| L17-8212 | Resolve Final Punchlist | 5 | 5 | 08-Dec-14 | 12-Dec-14 | 10 |
| L03-8214 | Floor Complete | 0 | 0 | | 10-Dec-14 | 12 |
| L16-8214 | Floor Complete | 0 | 0 | | 12-Dec-14 | 10 |
| L17-8214 | Floor Complete | 0 | 0 | | 12-Dec-14 | 10 |
| **Mech Penthouse** | | | | | | |

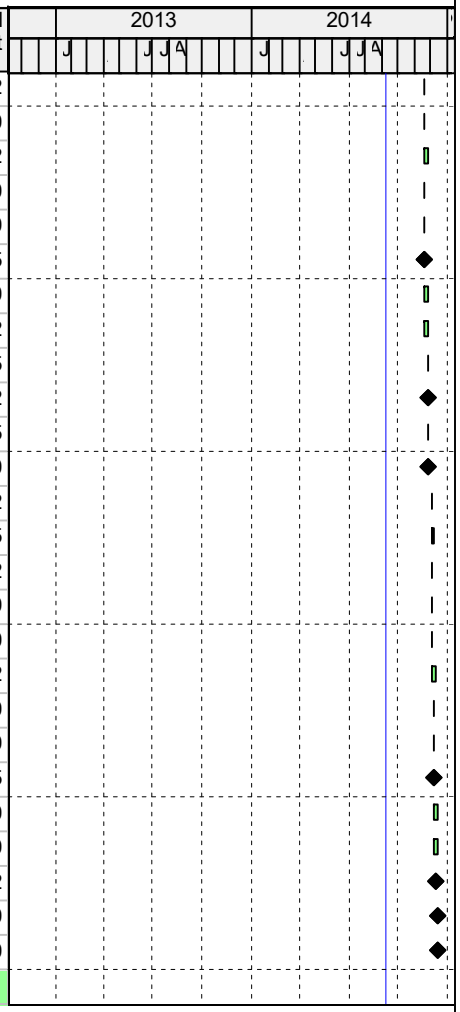



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-8102 | PH - Complete GWB Hang / Tape / Finish | 7 | 7 | 25-Sep-14 | 03-Oct-14 | 7 |
| PH-8100 | PH - Insulation | 3 | 3 | 25-Sep-14 | 29-Sep-14 | 7 |
| PH-8104 | PH - Int Painting | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 7 |
| PH-8122 | PH - Plumbing Trim / Finish | 10 | 10 | 10-Oct-14 | 23-Oct-14 | 7 |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 25 |
| PH-8114 | PH - Signage | 2 | 2 | 13-Oct-14 | 14-Oct-14 | 41 |
| PH-8108 | PH - Elec Trim / Finish | 10 | 10 | 24-Oct-14 | 06-Nov-14 | 7 |
| PH-8110 | PH - HVAC Trim / Finish | 10 | 10 | 24-Oct-14 | 06-Nov-14 | 11 |
| PH-8118 | PH - Elec Specialties Trim / Finish | 4 | 4 | 07-Nov-14 | 13-Nov-14 | 7 |
| PH-8124 | PH - Flooring | 4 | 4 | 14-Nov-14 | 19-Nov-14 | 7 |
| PH-8126 | PH - Doors & Hardware | 3 | 3 | 18-Nov-14 | 20-Nov-14 | 7 |
| PH-8134 | PH - Pre-Clean | 3 | 3 | 21-Nov-14 | 25-Nov-14 | 7 |
| PH-8132 | PH - Contractor Pre-Punchlist | 5 | 5 | 26-Nov-14 | 04-Dec-14 | 7 |
| PH-8208 | PH - Final Clean | 3 | 3 | 05-Dec-14 | 09-Dec-14 | 7 |
| PH-8210 | PH - Owner Walk / Create Punchlist | 1 | 1 | 10-Dec-14 | 10-Dec-14 | 7 |
| PH-8212 | PH - Final Punchlist | 5 | 5 | 11-Dec-14 | 17-Dec-14 | 7 |
| PH-8214 | PH - Floor Complete | 0 | 0 | | 17-Dec-14 | 7 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| **Smoke Control** | | | | | | |
| CO-7104 | Smoke Control Pre-Testing (Podium) | 5 | 5 | 09-Dec-14 | 15-Dec-14 | 4 |
| CO-7106 | City of Bellevue Smoke Control Testing (Podium) | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 4 |
| CO-7108 | Final Marriott Smoke Control Testing | 5 | 5 | 23-Dec-14 | 31-Dec-14 | 4 |
| **Fire Sprinklers** | | | | | | |
| CO-7110 | Fire Sprinkler Pre-Testing (Podium) | 5 | 5 | 09-Dec-14 | 15-Dec-14 | 4 |
| CO-7112 | City of Bellevue Fire Sprinkler Inspection / Approval (F | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 4 |
| CO-7114 | Marriott Fire Sprinkler Testing | 5 | 5 | 23-Dec-14 | 31-Dec-14 | 4 |
| **Fire Alarm** | | | | | | |

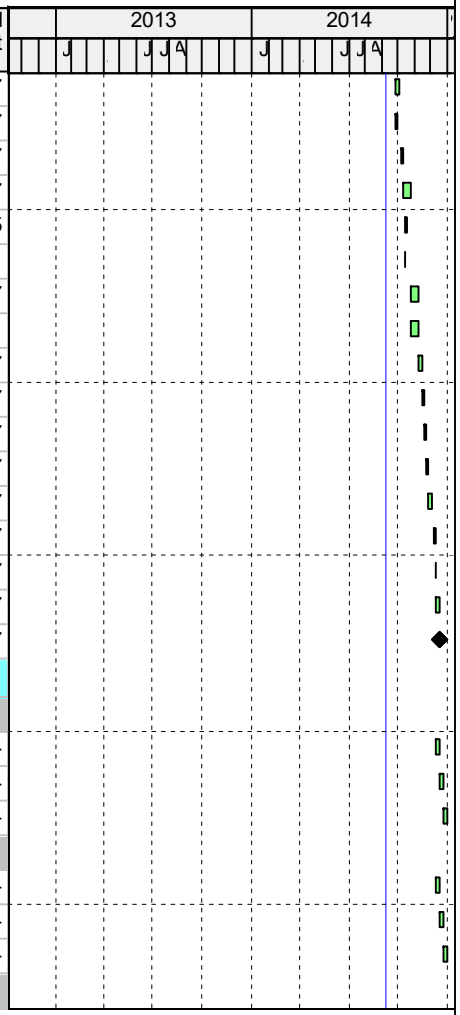



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7116 | Fire Alarm Pre-Testing (Podium) | 5 | 5 | 09-Dec-14 | 15-Dec-14 | 4 |
| CO-7118 | City of Bellevue Fire Alarm Inspection / Approval (Pod | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 4 |
| CO-7120 | Marriott Fire Alarm Testing | 5 | 5 | 23-Dec-14 | 31-Dec-14 | 4 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| CO-7100 | CO - Preliminary Start-Up & Testing (Podium) | 5 | 5 | 05-Nov-14 | 12-Nov-14 | 20 |
| CO-7102 | CO - HVAC Commissioning (Podium) | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 25 |

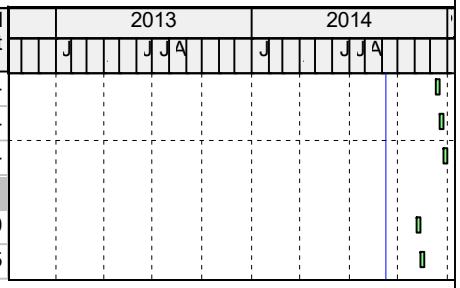



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Working Schedule - 10-4-14 Update (DRAFT)** | | | | | | |
| L09-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-04 A | 30-Sep-14 A | |
| I-1500 | Owner release revised LV design - Tower (ASIs 5, 13, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-1550 | Owner release revised LV design - Podium (ASIs 5, 1 | 200 | 0 | 23-May-13 A | 28-Apr-14 A | |
| I-1900 | Owner issue design revisions (ASIs 4, 9, 19, 34) | 215 | 0 | 23-May-13 A | 24-Mar-14 A | |
| I-2500 | Owner issue LL1 electrical revisions (ASIs 7, 9r2, 14, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-3400 | Owner provide Level 2 ceiling heights | 180 | 0 | 24-Jun-13 A | 24-Mar-14 A | |
| I-3700 | Owner resolve wall condition between stair and Eleva | 200 | 0 | 27-Jun-13 A | 16-Jun-14 A | |
| MM-1000 | MM - Temporary Power Available | 0 | 0 | 08-Jul-13 A | | |
| I-2100 | Owner revise roof steel design (Submittals 365, 370, | 200 | 0 | 09-Jul-13 A | 07-Apr-14 A | |
| I-2200 | Owner resolve elevator steel issue (RFI 112, RFI 112. | 200 | 0 | 09-Jul-13 A | 03-Mar-14 A | |
| I-2400 | Owner provide Tower light fixture selections (ASI 36) | 185 | 0 | 18-Jul-13 A | 08-Apr-14 A | |
| I-2900 | Owner revise Food Service and Kitchen (ASIs 11, 12, | 140 | 0 | 08-Aug-13 A | 27-Feb-14 A | |
| I-1400 | Owner develop envelope redesign | 70 | 0 | 27-Aug-13 A | 12-Dec-13 A | |
| I-3600 | Owner closeout glass/glazing allowance | 160 | 0 | 04-Sep-13 A | 30-Apr-14 A | |
| I-1200 | Owner release revised Concierge Lounge design (AS | 160 | 0 | 06-Sep-13 A | 08-Apr-14 A | |
| I-2800 | Owner revise interior public space design (ASIs 16, 18 | 130 | 0 | 25-Sep-13 A | 09-Apr-14 A | |
| I-2000 | Owner approve door frames (Submittals 258, 454, 48 | 85 | 0 | 27-Sep-13 A | 23-Jan-14 A | |
| I-3100 | Owner revise ballroom ceiling design (ASIs 18, 25) | 100 | 0 | 17-Oct-13 A | 25-Feb-14 A | |
| I-1600 | Owner provide directive for south & east corridor encl | 110 | 0 | 28-Oct-13 A | 18-Apr-14 A | |
| I-2300 | Owner resolve fire smoke dampers issue (RFI 233) | 115 | 0 | 30-Oct-13 A | 11-Apr-14 A | |
| I-2600 | Owner resolve L2 slab coordination issue | 4 | 0 | 13-Nov-13 A | 16-Nov-13 A | |
| I-2700 | Owner revise tower guest rooms design (ASIs 23, 29) | 58 | 0 | 04-Dec-13 A | 26-Feb-14 A | |
| I-1700 | Owner provide design for dry site utilities (ASIs 20, 20 | 66 | 0 | 09-Dec-13 A | 13-Mar-14 A | |
| I-1402 | Begin exterior panel production | 41 | 0 | 13-Dec-13 A | 12-Feb-14 A | |
| I-1300 | Owner issue "Hold" directive (email) | 0 | 0 | | 19-Dec-13 A | |
| I-1100 | Owner release revised L17 design (ASI 23, 29R1) | 74 | 0 | 20-Dec-13 A | 08-Apr-14 A | |

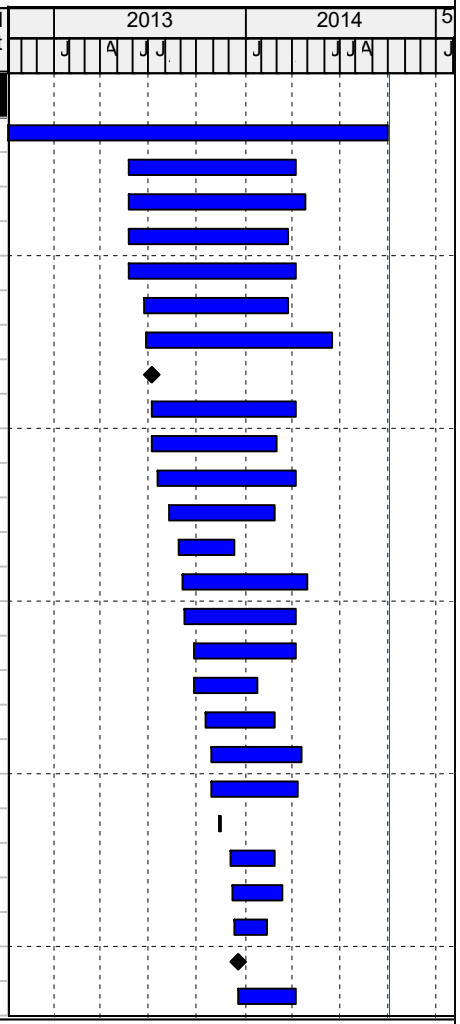


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| High Rise Hotel Sample Project | All Activities | Schedule Status Date 06-Oct-14 |
|---|---|---|

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1302 | Owner issue ASI 30 (Prep Kitchen Revisions) | 47 | 0 | 20-Dec-13 A | 27-Feb-14 A | |
| I-1404 | City of Bellevue Approval | 90 | 0 | 23-Dec-13 A | 15-Jul-14 A | |
| I-3000 | Owner revise bar area (change to straight bar, IDRFI-( | 71 | 0 | 22-Jan-14 A | 27-May-14 A | |
| I-1306 | Prep Kitchen - Additional plumbing (ASI 30) | 4 | 0 | 17-Feb-14 A | 01-Aug-14 A | |
| I-2202 | Fabricate revised elevator steel | 60 | 0 | 04-Mar-14 A | 07-May-14 A | |
| I-2704 | Framing "Go Back" work for ASIs 23, 29 - L4 | 1 | 0 | 05-Mar-14 A | 12-Mar-14 A | |
| I-3900 | RFI 471, Resolve Ballroom parapet height issue | 1 | 0 | 08-Mar-14 A | 07-May-14 A | |
| I-1702 | Owner provide directive to proceed | 26 | 0 | 14-Mar-14 A | 01-May-14 A | |
| I-3300 | Owner provide Guest Room plumbing fixture selectio | 1 | 0 | 20-Mar-14 A | 20-Mar-14 A | |
| I-1902 | Procure revised structural steel | 15 | 0 | 25-Mar-14 A | 14-Apr-14 A | |
| I-4000 | Owner complete design of east stitched enclosure (fo | 1 | 0 | 01-Apr-14 A | 14-May-14 A | |
| I-2102 | Fabricate revised roof steel | 20 | 0 | 08-Apr-14 A | 15-May-14 A | |
| I-3200 | Owner provide light fixture selections for podium level | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| I-3800 | Resolve Heat Pump Electrical Overcurrent Issue | 20 | 0 | 23-Apr-14 A | 18-Jun-14 A | |
| L10-8221 | HVAC Risers Duct Insulation | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L11-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| I-2304 | Framing "Go Back" work at L3 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2306 | Framing "Go Back" work at L4 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2308 | Framing "Go Back" work at L5 for RFI 233 | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2706 | Framing "Go Back" work for ASIs 23, 29 - L5 | 1 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2708 | Framing "Go Back" work for ASIs 23, 29 - L6 | 1 | 0 | 29-Apr-14 A | 09-May-14 A | |
| I-2702 | Framing "Go Back" work for ASIs 23, 29 - L3 | 1 | 0 | 01-May-14 A | 01-May-14 A | |
| I-1706 | PSE scheduling delay | 10 | 0 | 01-May-14 A | 20-May-14 A | |
| I-3602 | Complete shop drawings & fab/deliver storefront fram | 40 | 0 | 01-May-14 A | 14-Jun-14 A | |
| L04-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| I-1802 | Rework framing for door hold-opens - LL4 | 1 | 0 | 07-May-14 A | 08-May-14 A | |

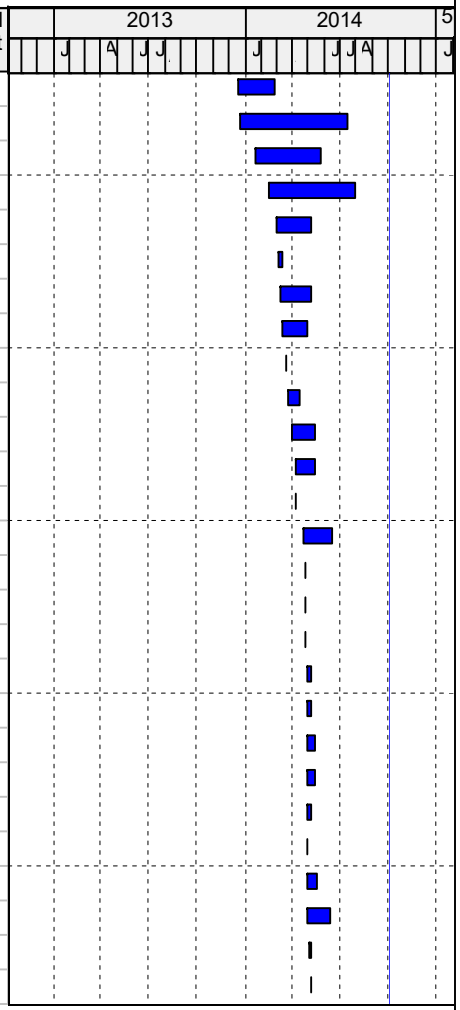


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-May-14 A | 12-May-14 A | |
| I-1800 | Owner issue directive to proceed with door hold-open | 1 | 0 | 08-May-14 A | 08-May-14 A | |
| I-1804 | Rework framing for door hold-opens - LL3 | 1 | 0 | 08-May-14 A | 09-May-14 A | |
| I-2312 | Framing "Go Back" work at L7 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-2314 | Framing "Go Back" work at L8 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-3902 | Install Ballroom parapet extension | 5 | 0 | 08-May-14 A | 13-May-14 A | |
| I-1806 | Rework framing for door hold-opens - LL2 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-1808 | Rework framing for door hold-opens - LL1 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-2310 | Framing "Go Back" work at L6 for RFI 233 | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| I-2710 | Framing "Go Back" work for ASIs 23, 29 - L7 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| L05-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L06-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L05-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| LL2E-8110 | LL2 - Electrical, Fire pumps/equipment final connectic | 5 | 1 | 12-May-14 A | 06-Oct-14 | 49 |
| PH-8704 | PH - Install Machine Support Steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| PH-8710 | Install elevator rail support steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| L03-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L03-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 13-May-14 A | 14-May-14 A | |
| I-4002 | East Stitched - Install framing and windows | 9 | 0 | 19-May-14 A | 09-Jun-14 A | |
| L10-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L11-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L12-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| RF-4038 | AR - Concrete pads and curbs | 5 | 0 | 21-May-14 A | 04-Jun-14 A | |
| L10-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L11-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L12-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |

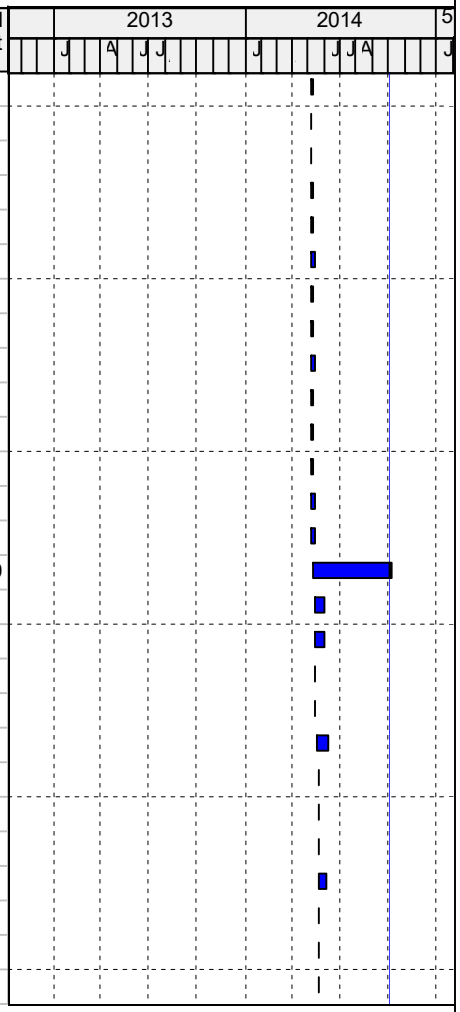



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L15-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 27-May-14 A | |
| L11-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 07-Jun-14 A | |
| L12-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 27-May-14 A | 06-Jun-14 A | |
| I-3002 | City of Bellevue approve bar design changes. | 5 | 2 | 28-May-14 A | 07-Oct-14 | 1 |
| L16-8221 | HVAC Risers Duct Insulation | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| PH-8712 | PH - Complete Framing and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| PH-8714 | Stage PH/L18 roofing materials | 2 | 0 | 30-May-14 A | 30-May-14 A | |
| L08-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L08-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 02-Jun-14 A | 20-Jun-14 A | |
| PH-8704I | Correct support steel embeds | 2 | 0 | 02-Jun-14 A | 11-Jun-14 A | |
| L14-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 03-Jun-14 A | 04-Jun-14 A | |
| L17-8221 | HVAC Risers Duct Insulation | 1 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| PC-4010 | PC - Fireproof Entry Roof Steel | 5 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| I-4100 | Owner resolve trap primers issue (RFI 560) | 5 | 0 | 03-Jun-14 A | 20-Jun-14 A | |
| RF-6028 | Tower Roof - Structural Steel | 5 | 0 | 04-Jun-14 A | 17-Jun-14 A | |
| L14-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L1B-6005 | Head of Wall Fire Caulk at CMU (including East Servi | 2 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L14-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L15-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |

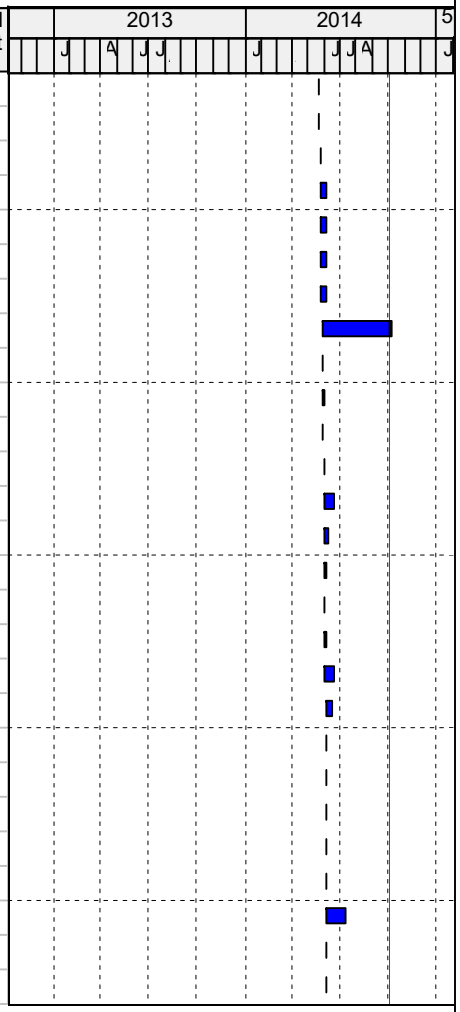


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L09-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 11-Jun-14 A | 12-Jun-14 A | |
| I-3702 | Complete wall framing at Stair/Elevator 5 (LL4) | 2 | 0 | 18-Jun-14 A | 20-Jun-14 A | |
| I-3720 | Fireproof added steel between Stair 1 and Elevator 5 | 5 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| I-3722 | Complete GWB between Stair 1 and Elevator 5 shaft | 10 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| LL1-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 22-Jul-14 A | |
| TC-5912 | Tower Crane pour-backs (LL4 to L3) | 4 | 0 | 19-Jun-14 A | 26-Jun-14 A | |
| LL1-Z2-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL4-6005 | LL4 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| LL3-6005 | LL3 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| L03-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 21-Jun-14 A | 21-Jun-14 A | |
| L06-6040 | Test Heat Pumps - L3, L4, L5 and L6 | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L03-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| L17-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL2-6005 | LL2 - Seismic Head Of Wall Fire Caulk at CMU | 5 | 0 | 24-Jun-14 A | 18-Jul-14 A | |
| I-3704 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL1-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z2-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z3-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 04-Aug-14 A | |
| L1L-6005 | Head of Wall Fire Caulk at CMU (including back of ho | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1K-6005 | Head of Wall Fire Caulk at CMU & Inspection | 2 | 0 | 24-Jun-14 A | 08-Aug-14 A | |
| L03-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L04-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| I-3710 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| I-3712 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| L1K-6018a | Install Kitchen hoods and grease ducts (OFCI) | 10 | 2 | 25-Jun-14 A | 07-Oct-14 | 19 |

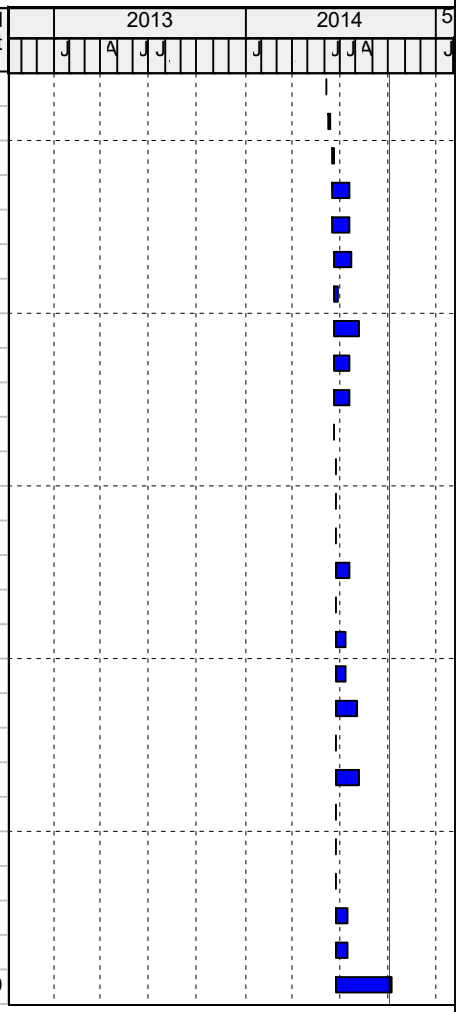


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8604 | L3 Pool - Plumbing R/I | 5 | 3 | 25-Jun-14 A | 20-Nov-14 | 9 |
| L04-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 26-Jun-14 A | 03-Jul-14 A | |
| L09-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 26-Jun-14 A | 26-Jun-14 A | |
| I-3706 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 26-Jun-14 A | 10-Jul-14 A | |
| L03-8600 | L3 Pool - Framing & HM frames | 5 | 2 | 26-Jun-14 A | 17-Nov-14 | 9 |
| L05-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L08-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L04-7018 | Electrical Rough-In | 1 | 0 | 27-Jun-14 A | 22-Jul-14 A | |
| L04-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 27-Jun-14 A | 23-Jul-14 A | |
| L03-7020 | HVAC Rough-In | 1 | 0 | 29-Jun-14 A | 15-Jul-14 A | |
| L1RR-8100 | Insulation [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8100 | Insulation [DELETED - included in Ballroom activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8100 | Insulation [DELETED - included in Meeting Rooms ac | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8102 | GWB Hang [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8215 | GWB Tape [DELETED - included in Meeting Rooms a | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8104 | Prime Paint [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8102 | GWB Hang [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8215 | GWB Tape [DELETED - included in Ballroom activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8104 | Prime Paint [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |

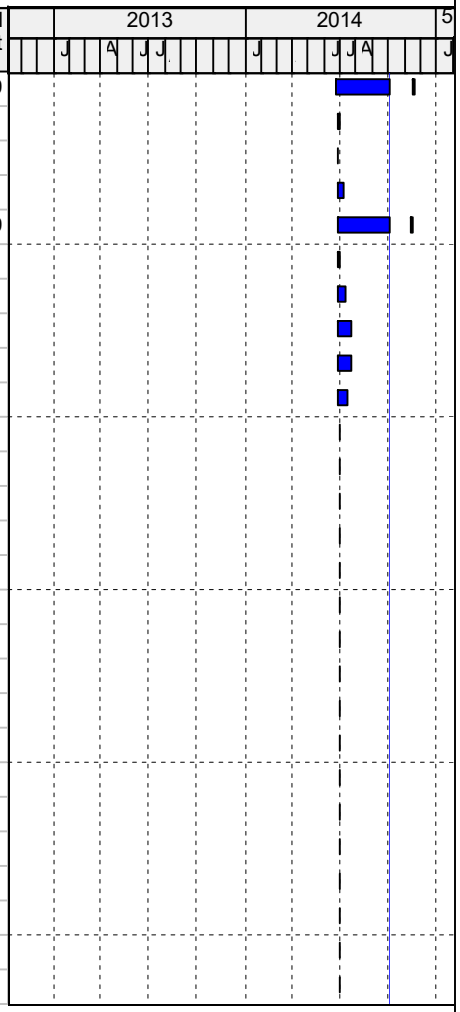


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1RR-8102 | GWB Hang [DELETED - included in Kitchen activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8215 | GWB Tape [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8104 | Prime Paint [DELETED - included in Kitchen activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L03-7018 | Electrical Rough-In | 1 | 0 | 01-Jul-14 A | 14-Jul-14 A | |
| L03-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Jul-14 A | 15-Jul-14 A | |
| L10-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7102 | Install Vertical Heat Pump | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L03-7116 | Frame Walls | 1 | 0 | 02-Jul-14 A | 14-Jul-14 A | |
| L03-7118 | Install HM Door Frame | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L04-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L05-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L07-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L08-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L09-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L10-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L12-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| I-3708 | Complete wall framing at Stair/Elevator 5 (LL3) | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |

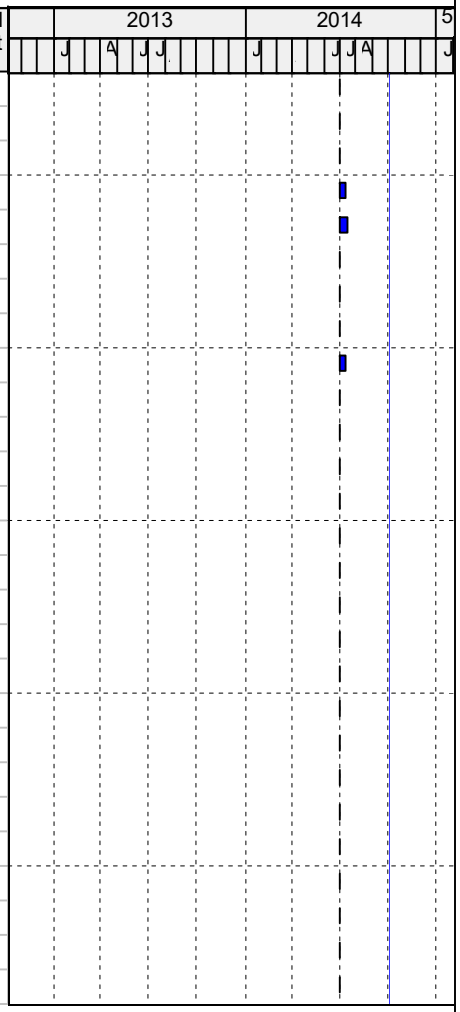



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L11-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 03-Jul-14 A | 07-Jul-14 A | |
| L04-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L05-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L06-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L07-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L08-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L17-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L10-6040 | Test Heat Pumps - L7, L8, L9 and L10 | 3 | 0 | 07-Jul-14 A | 09-Jul-14 A | |
| L10-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L03-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L04-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L05-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L06-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L07-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L08-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L09-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L10-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L12-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |

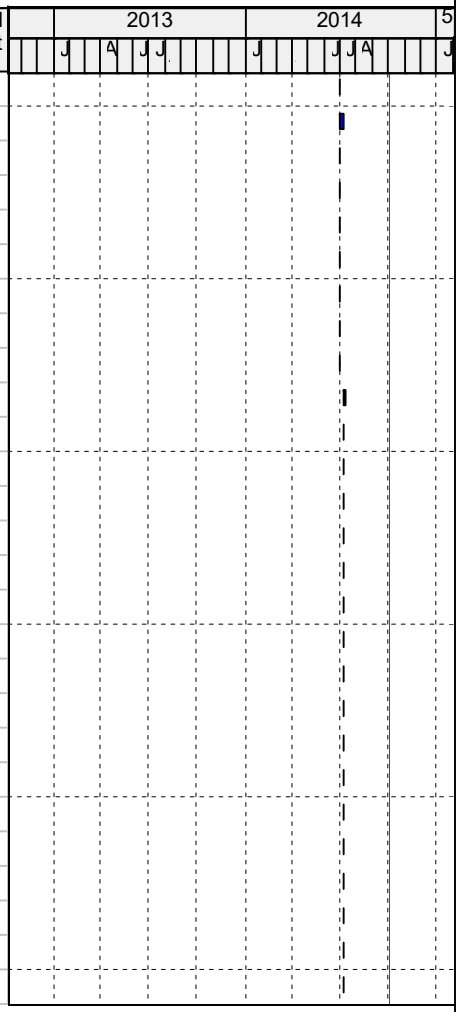



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L11-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Jul-14 A | 29-Jul-14 A | |
| L03-8602 | L3 Pool - Fire Sprinkler R/I | 5 | 0 | 08-Jul-14 A | 22-Jul-14 A | |
| L03-7016 | Install HM door frame | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L11-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L16-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 09-Jul-14 A | |
| L04-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |

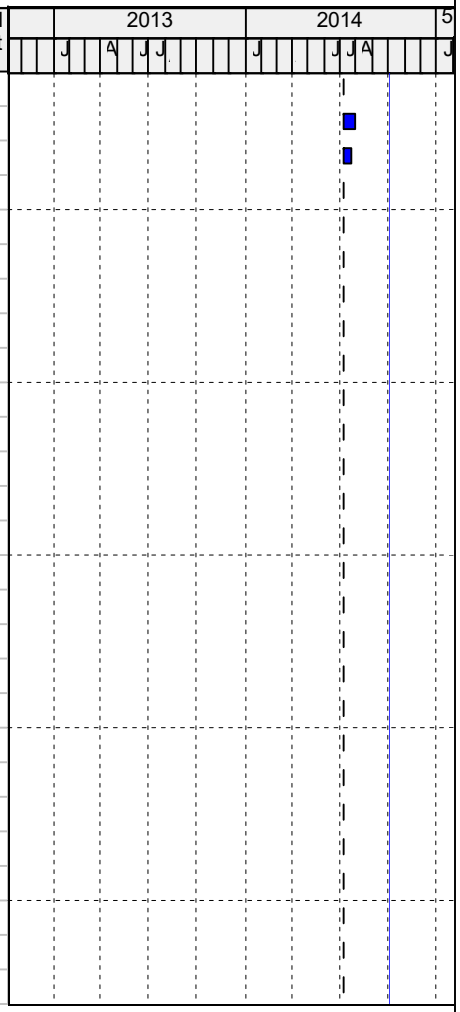



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L12-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| MP-FAB1 | Fabricate and Deliver Bronze Gold Horizontal Panels | 30 | 0 | 09-Jul-14 A | 15-Jul-14 A | |
| L04-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L05-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L06-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L16-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| MP-FAB2 | Fabricate and Deliver Silver Vertical Panels | 45 | 0 | 10-Jul-14 A | 25-Aug-14 A | |
| I-3004 | Issue ASI 38 | 0 | 0 | 11-Jul-14 A | | |
| I-3006 | Release bar area for x-ray examination | 5 | 0 | 11-Jul-14 A | 03-Sep-14 A | |
| L07-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| LL1-Z2-6018a | Complete Mech RI at tower crane opening (LL1) | 4 | 0 | 14-Jul-14 A | 17-Jul-14 A | |
| L08-6223 | Frame Corridor Ceilings | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| SW-2006a | Complete Dry Utilities (Phase 2) | 5 | 0 | 14-Jul-14 A | 24-Jul-14 A | |
| L04-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L04-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L05-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L06-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |

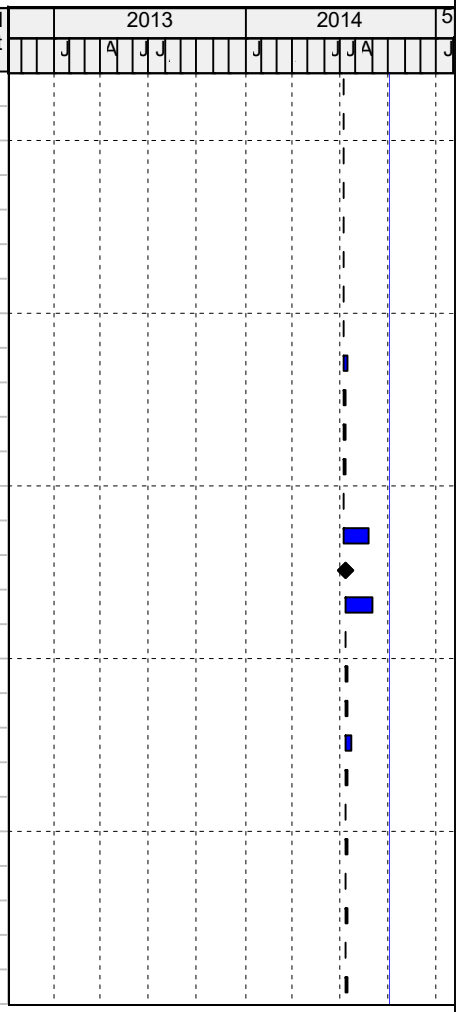



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L04-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L11-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L11-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L12-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L12-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L15-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L15-7102 | Install Vertical Heat Pump | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L1B-6026 | Install operable partition steel | 2 | 0 | 15-Jul-14 A | 08-Aug-14 A | |
| L09-6223 | Frame corridor ceilings | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L03-7120 | Electrical Rough-In | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |

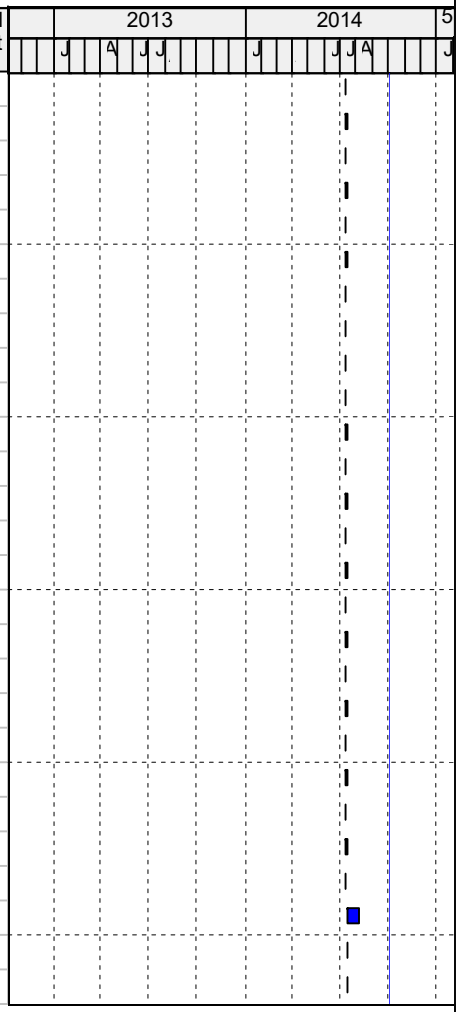



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L07-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L08-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L08-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L09-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L09-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L03-7142 | Install Laundry Chute (All Levels) | 9 | 0 | 15-Jul-14 A | 25-Jul-14 A | |
| LL2-2045 | LL2 - Electrical Room build-out | 15 | 0 | 15-Jul-14 A | 26-Sep-14 A | |
| L03-7122 | HVAC Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L04-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L05-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L06-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L07-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L07-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L08-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L08-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L09-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L09-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |

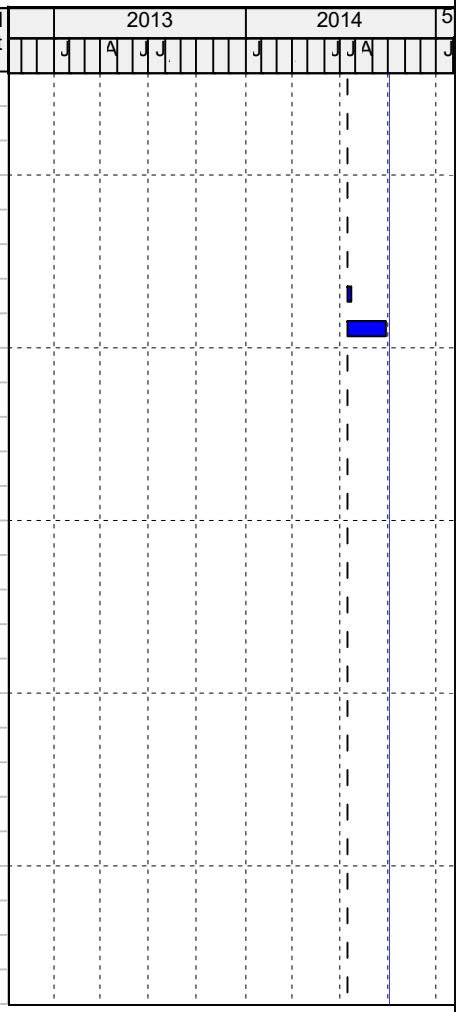



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L11-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L11-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L12-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L12-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L15-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L15-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L16-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L17-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L04-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L04-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L05-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L05-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L06-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L06-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L07-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L08-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L09-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |

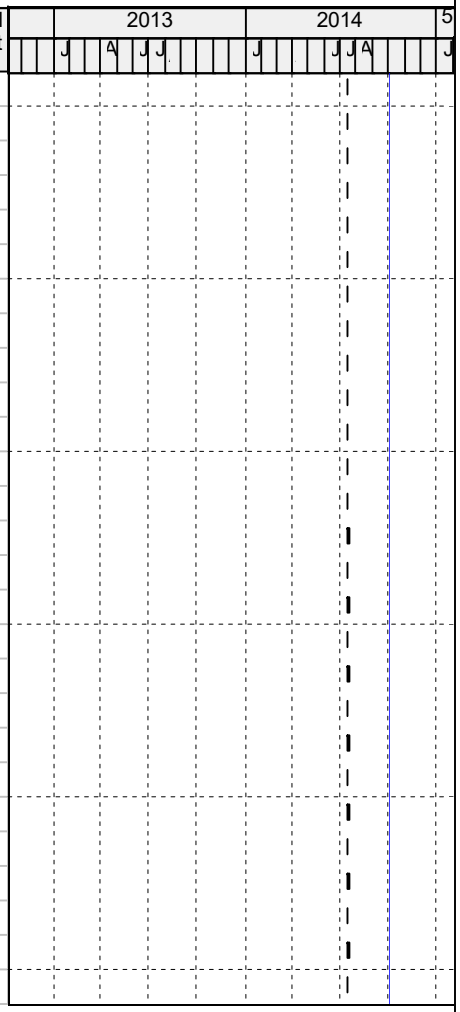



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L11-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L11-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L12-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L12-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L16-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L03-8608 | L3 Pool - Electrical R/I | 5 | 2 | 18-Jul-14 A | 19-Nov-14 | 10 |
| L03-8610 | L3 Pool - Fire Alarm / Elec Specialties R/I | 5 | 3 | 18-Jul-14 A | 20-Nov-14 | 9 |
| L15-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L15-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| L17-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L17-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| LL2-2052 | LL2 - Install fuel piping and exhaust duct to Generatc | 8 | 0 | 21-Jul-14 A | 15-Aug-14 A | |
| L04-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L04-7016 | Install HM door frame | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L07-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L08-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L10-7116 | Frame Walls | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L16-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 21-Jul-14 A | 22-Jul-14 A | |
| L16-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |

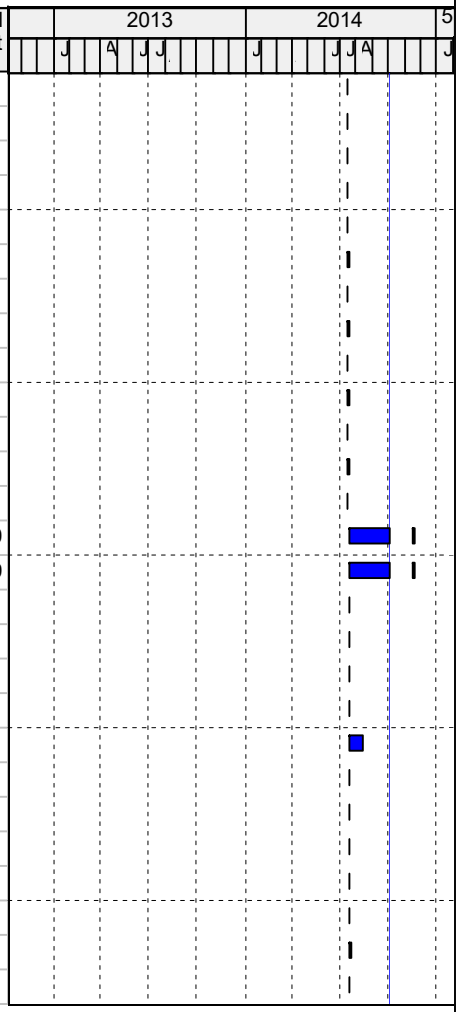



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| MPT-1002 | Tower - Install Elevation 35 (east elevation-south half) | 8 | 0 | 25-Jul-14 A | 04-Aug-14 A | |
| L16-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 25-Jul-14 A | 25-Jul-14 A | |
| L11-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L14-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L15-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L16-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L10-6223 | Frame Corridor Ceilings | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L11-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L15-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L15-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L11-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L14-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L16-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| I-1304 | Prep Kitchen - Additional framing (ASI 30) | 2 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-2302 | Framing "Go Back" work at LL1 for RFI 233 | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| I-2502 | Electrical rework at LL1 for ASIs 7, 9r2, 14, 27 | 4 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| L12-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L1B-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 01-Aug-14 A | 15-Aug-14 A | |
| MPL4-1000 | Upper L4 Ballroom - Install Elevations 1, 2 & 3 (south | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1000 | Tower - Install Elevations 26-27 (west elevation) [DEL | 13 | 0 | 01-Aug-14 A | 01-Aug-14 A | |

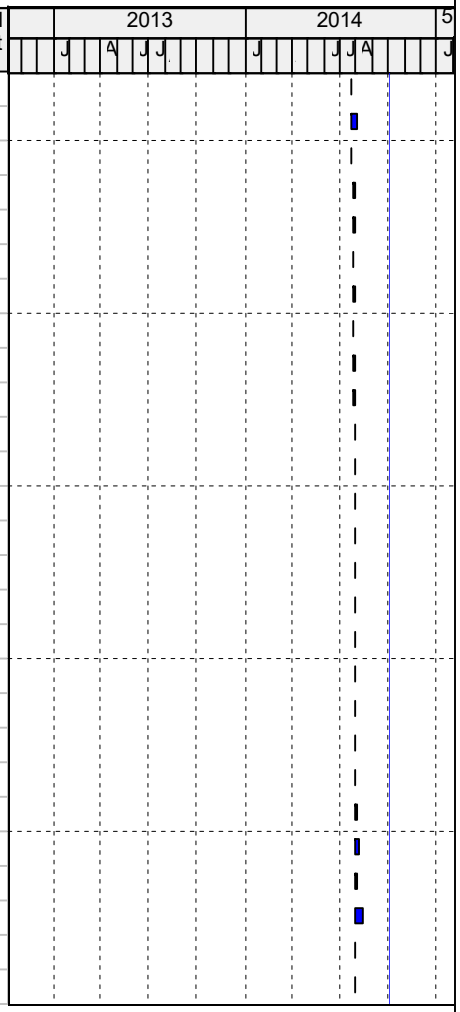



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPP-1002 | Podium - Install Elevations 1 & 2 (west elevation, sou | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPP-1008 | Podium - Install Elevations 7 & 8 (north & east elevati | 9 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1002 | Upper L4 Ballroom - Install Elevation 10 (west elevatic | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1004 | Upper L4 Ballroom - Install Elevation 9 (north elevatio | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1006 | Tower - Install Elevation 40 (east return-east end) [DE | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1010 | Tower - Install Elevations 51 (north elevation) [DELET | 8 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-4004 | East Stitched - Install metal panels [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L11-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L11-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L15-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L14-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L17-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| MPT-1010b | Tower - Install Elevation 45 [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L16-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 04-Aug-14 A | 05-Aug-14 A | |
| L11-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Aug-14 A | 08-Aug-14 A | |
| L04-7020 | HVAC Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |

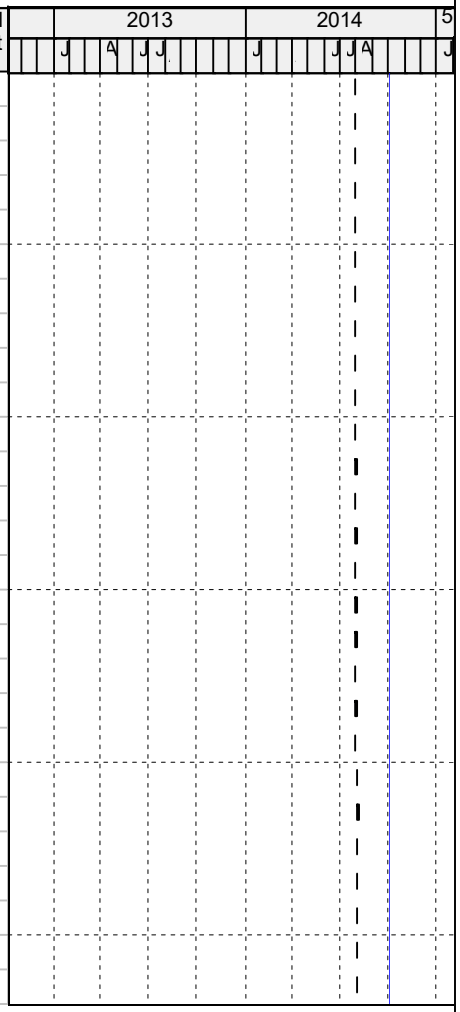



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L14-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L15-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 05-Aug-14 A | 07-Aug-14 A | |
| L05-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L06-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L07-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L08-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L09-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L10-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7018 | Electrical Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L14-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 05-Aug-14 A | 06-Aug-14 A | |
| L14-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| I-4104 | Install added trap primers - LL1 | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L06-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L07-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L08-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L09-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |

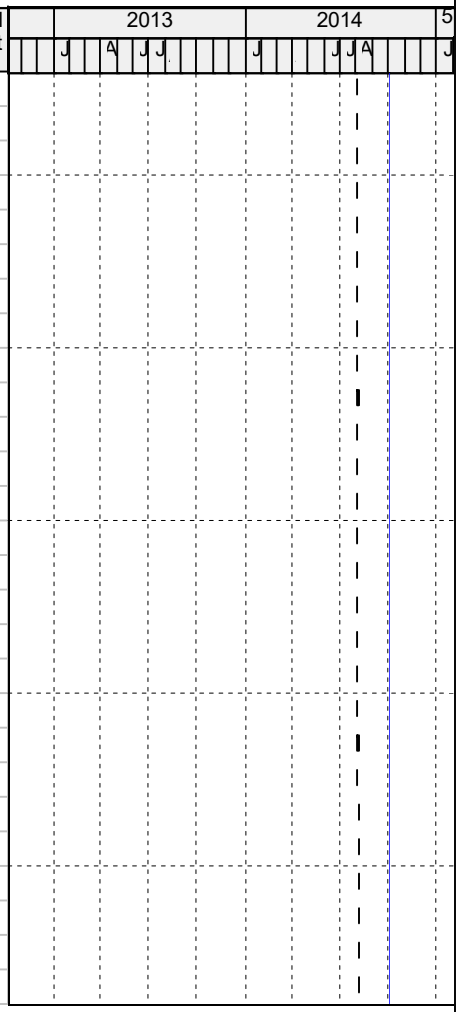



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7020 | HVAC Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L16-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| EL-1220 | Elevator fronts delivered | 0 | 0 | 07-Aug-14 A | | |
| L12-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L12-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-6223 | Frame Corridor Ceilings | 4 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L11-7016 | Install HM door frame | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L12-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L15-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L15-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L16-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L16-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L17-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L17-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-6040 | Test Heat Pumps - L11, L12 and L14 | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| PH-6026 | PH - Insulation/Vapor Barrier/GWB at Exterior Walls | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |

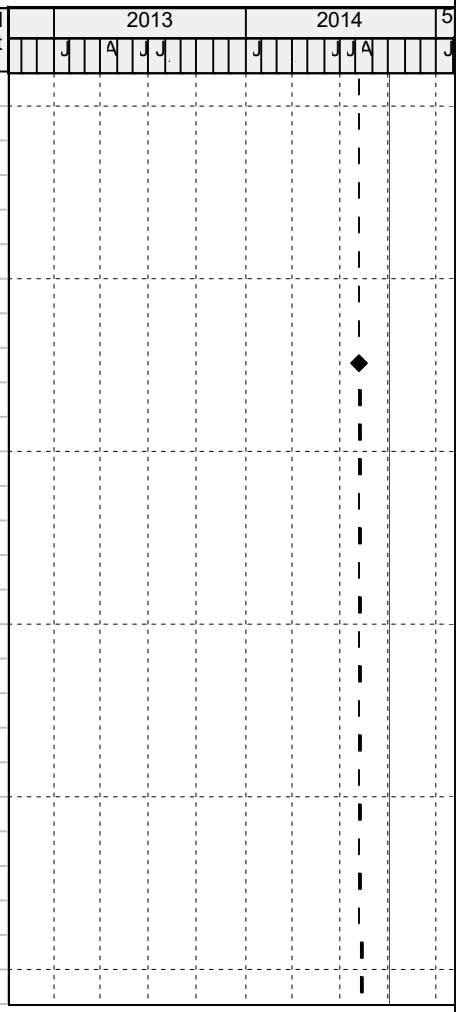



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L11-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-7026 | Inspections for GWB Cover | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 13-Aug-14 A | 13-Aug-14 A | |
| L15-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 14-Aug-14 A | 15-Aug-14 A | |
| LL2E-8108 | LL2 - Set fire pumps and equipment | 5 | 0 | 14-Aug-14 A | 29-Sep-14 A | |
| L10-7028 | GWB Hang/Tape/Finish | 5 | 2 | 14-Aug-14 A | 07-Oct-14 | 43 |
| L12-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L12-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L16-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L1BOH2-6008 | Int Wall Framing & Inspection | 5 | 0 | 14-Aug-14 A | 20-Aug-14 A | |
| I-4106 | Install added trap primers - L1 | 1 | 0 | 15-Aug-14 A | 15-Aug-14 A | |
| L14-6223 | Frame Corridor Ceilings | 4 | 0 | 15-Aug-14 A | 16-Aug-14 A | |
| L03-8136 | Install Counter Subtops | 3 | 0 | 15-Aug-14 A | 18-Aug-14 A | |
| LL2-2054 | LL2 - GWB, Hang 1st Layer at Laundry Room | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| LL2E-8112 | LL2 - Form/Pour Fire Pump Pads/Curbs | 2 | 0 | 16-Aug-14 A | 18-Aug-14 A | |
| LL1-6014Ia | L1 bar redesign - rework plumbing at ceilings | 10 | 5 | 18-Aug-14 A | 10-Oct-14 | 19 |

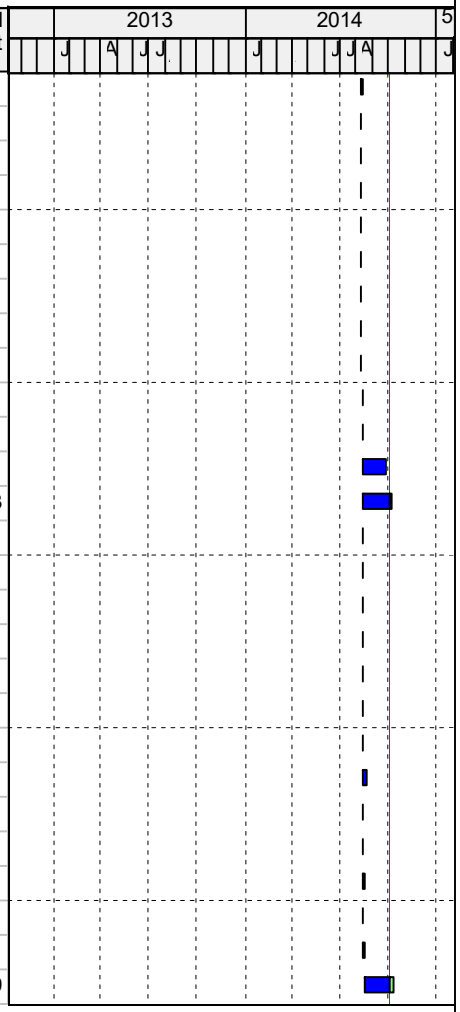



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6223 | Frame Corridor Ceilings | 4 | 0 | 18-Aug-14 A | 21-Aug-14 A | |
| L17-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Aug-14 A | 18-Aug-14 A | |
| L04-8136 | Install Counter Subtops | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-6014Ic | L1 bar redesign - rework electrical at ceilings | 10 | 5 | 18-Aug-14 A | 10-Oct-14 | 23 |
| LL2E-8114 | LL2 - Set Tube Steel at Door | 1 | 0 | 19-Aug-14 A | 19-Aug-14 A | |
| L17-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 20-Aug-14 A | 21-Aug-14 A | |
| L17-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 20-Aug-14 A | 20-Aug-14 A | |
| L05-8136 | Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 26-Aug-14 A | |
| L06-8136 | Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 25-Aug-14 A | |
| L16-6223 | Frame Corridor Ceilings | 4 | 0 | 21-Aug-14 A | 29-Aug-14 A | |
| L17-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 21-Aug-14 A | 22-Aug-14 A | |
| L17-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 21-Aug-14 A | 21-Aug-14 A | |
| L1BOH2-6016 | Electrical RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6018 | HVAC RI | 4 | 1 | 21-Aug-14 A | 06-Oct-14 | 32 |
| L15-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7020 | HVAC Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7022 | Fire Sprinkler Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| LL2E-8116 | LL2 - Set Door Jamb | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L04-7028 | GWB Hang/Tape/Finish | 5 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L05-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L05-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L06-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |

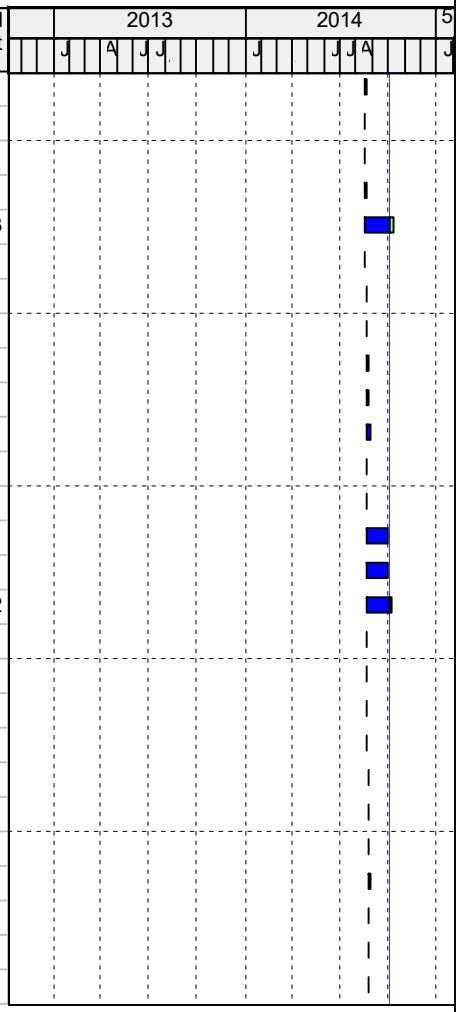



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L03-8123 | Bathroom "Barn Doors" On Site | 0 | 0 | 25-Aug-14 A | | |
| LL3-6026 | LL3 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL2-6026 | LL2 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL1-Z3-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L1BOH2-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |

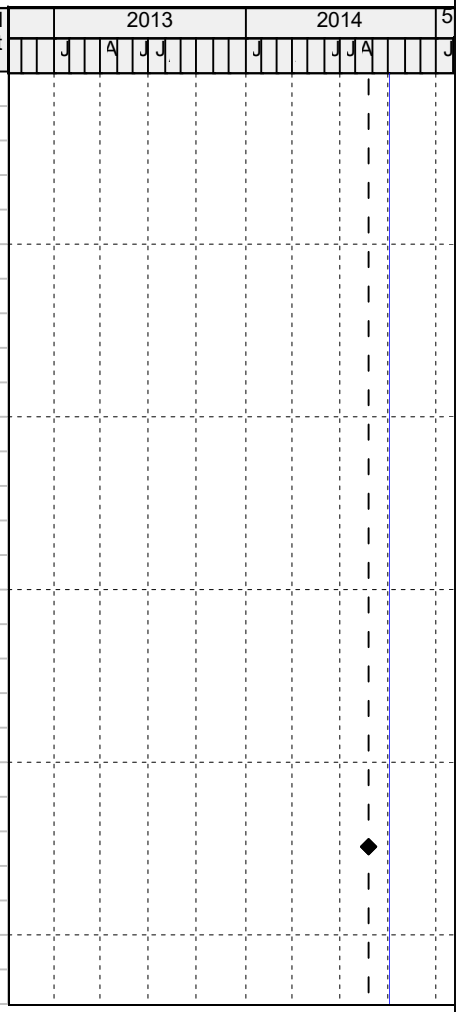



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-6026 | L2 - Set Elevator Fronts (Cars 1-4 | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L03-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L04-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L05-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L06-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L07-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L08-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L09-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L10-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L11-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L12-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L14-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L15-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L16-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L17-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| MPT-1008 | Tower - Install E/W Wing, N. Side West Half (Elev 50, | 7 | 0 | 26-Aug-14 A | 03-Oct-14 A | |
| L06-6005 | CMU Fire Caulk/Clips | 2 | 1 | 26-Aug-14 A | 06-Oct-14 | 26 |
| L07-6005 | CMU Fire Caulk/Clips | 2 | 1 | 26-Aug-14 A | 06-Oct-14 | 26 |
| L08-6005 | CMU Fire Caulk/Clips | 2 | 1 | 26-Aug-14 A | 06-Oct-14 | 26 |
| L05-7026 | Inspections for GWB Cover | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L05-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L11-7028 | GWB Hang/Tape/Finish | 5 | 2 | 26-Aug-14 A | 07-Oct-14 | 43 |
| L12-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L14-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L03-8105a | Painting - Split Door Jambs | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L09-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 06-Oct-14 | 26 |
| L10-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 06-Oct-14 | 26 |

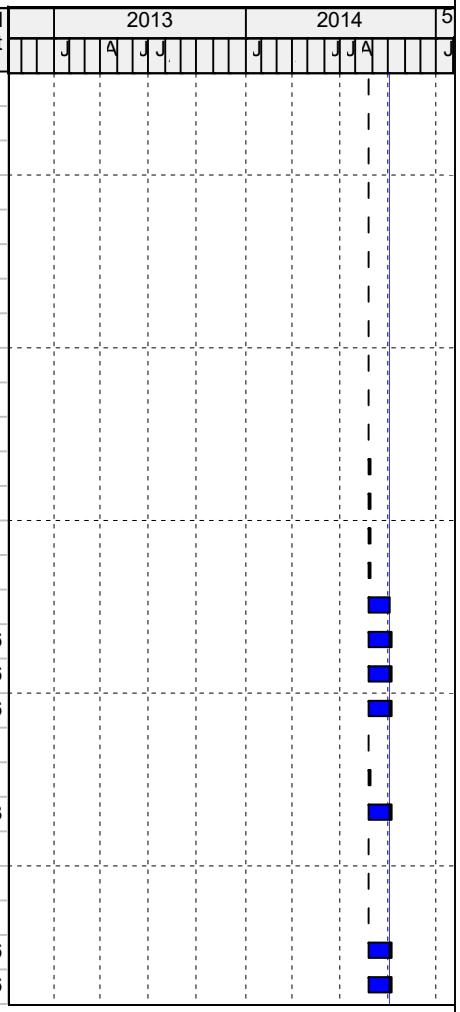


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 07-Oct-14 | 26 |
| L12-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 07-Oct-14 | 26 |
| L14-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 07-Oct-14 | 26 |
| L15-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 07-Oct-14 | 26 |
| L16-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 07-Oct-14 | 26 |
| L05-8201 | Install ACT Grid @ Corridors | 2 | 0 | 27-Aug-14 A | 28-Aug-14 A | |
| L16-7022 | Fire Sprinkler Rough-In | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L04-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L06-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| EP-5110a | L1 - Install Steel at Revolving Door Opening | 3 | 0 | 27-Aug-14 A | 29-Aug-14 A | |
| L05-8105a | Painting - Split Door Jambs | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| I-4102 | Install added trap primers - LL2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4108 | Install added trap primers - L2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4110 | Install added trap primers - L3 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4112 | Install added trap primers - Roof PH | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| L03-8124d | Flooring On Site and Acclimated | 2 | 0 | 29-Aug-14 A | 01-Sep-14 A | |
| L02-5102 | L2 - Storefront Frames | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| L04-6005 | CMU Fire Caulk/Clips | 2 | 1 | 02-Sep-14 A | 06-Oct-14 | 26 |
| L05-6005 | CMU Fire Caulk/Clips | 2 | 1 | 02-Sep-14 A | 06-Oct-14 | 26 |
| L17-6005 | CMU Fire Caulk/Clips | 2 | 1 | 02-Sep-14 A | 07-Oct-14 | 26 |
| L03-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L12-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L14-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L07-8136 | Install Counter Subtops | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| LL1-Z3-FCC10 | FCC - Set Jamb | 1 | 0 | 02-Sep-14 A | 03-Sep-14 A | |
| MPT-1004 | Tower - Install E/W Wing, S. Side w/o Windows (Elev | 10 | 8 | 03-Sep-14 A | 15-Oct-14 | 44 |
| L03-7028 | GWB Hang/Tape/Finish | 5 | 2 | 03-Sep-14 A | 07-Oct-14 | 43 |

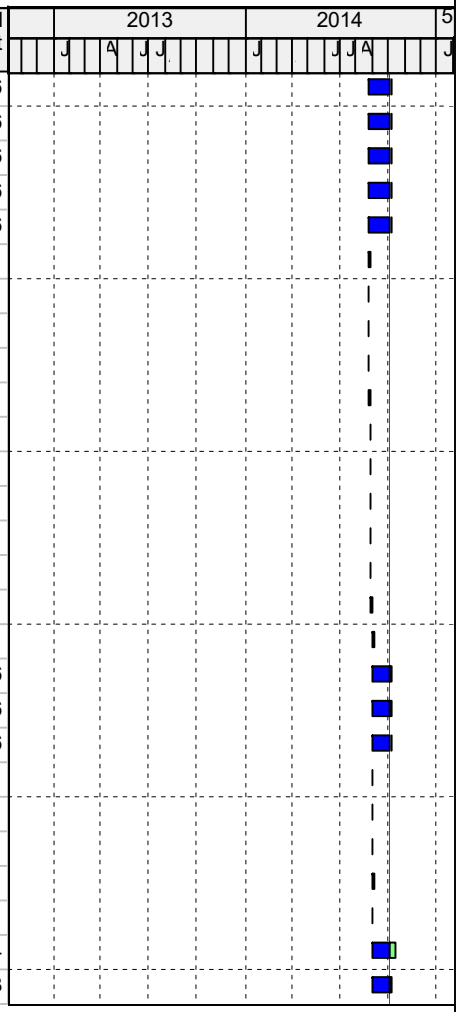



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7028 | GWB Hang/Tape/Finish | 5 | 2 | 03-Sep-14 A | 07-Oct-14 | 43 |
| L03-8126a | Doors & Hardware On Site | 0 | 0 | 03-Sep-14 A | | |
| LL1-Z3-FCC12 | FCC - Sheetrock Outside Wall | 1 | 0 | 03-Sep-14 A | 03-Sep-14 A | |
| L16-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| L17-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Sep-14 A | 11-Sep-14 A | |
| L02-5104b | L2 - Install Storefront Temporary Enclosures | 1 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| LL1-Z3-FCC14 | FCC - Verify Fire Caulk OK & Inspect Room OK to 2n | 1 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| I-3008 | Coordinate and perform x-ray examination | 7 | 0 | 04-Sep-14 A | 12-Sep-14 A | |
| L02-5104a | L2 - Measure/Fabricate Storefront Glazing | 15 | 0 | 05-Sep-14 A | 18-Sep-14 A | |
| LL1-Z3-FCC16 | FCC - GWB, Hang 2nd Layer | 2 | 0 | 05-Sep-14 A | 08-Sep-14 A | |
| L03-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L15-7018 | Electrical Rough-In | 1 | 0 | 08-Sep-14 A | 08-Sep-14 A | |
| EL-1228 | Construct/Approve elevator lobby framing mockup (L | 3 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| LL2E-8118 | LL2 - Frame Infill, Install Densglass & Inspect at Fire I | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L06-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L08-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L15-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7018 | Electrical Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L3-5104a | L3 - Measure/Fabricate Storefront Glazing | 15 | 0 | 09-Sep-14 A | 30-Sep-14 A | |
| L03-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 23-Sep-14 A | |
| L03-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L04-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L06-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| L08-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |

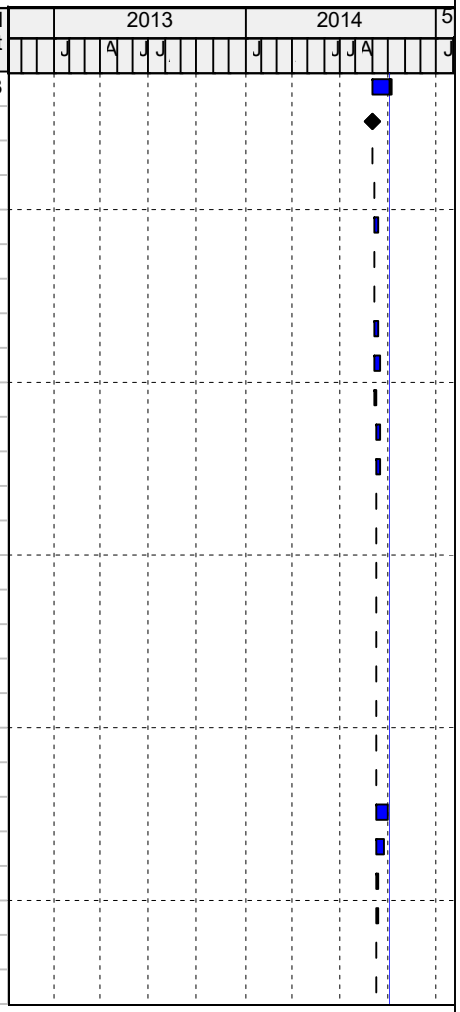



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L06-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L06-7028 | GWB Hang/Tape/Finish | 5 | 2 | 10-Sep-14 A | 07-Oct-14 | 43 |
| L08-7028 | GWB Hang/Tape/Finish | 5 | 2 | 10-Sep-14 A | 07-Oct-14 | 43 |
| L15-7026 | Inspections for GWB Cover | 1 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| LL2E-8120 | LL2 - Insulation, Vapor Barrier & Inspect at Fire Pump | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L08-8395 | Framing at Elevator Lobby | 4 | 0 | 11-Sep-14 A | 17-Sep-14 A | |
| L15-7028 | GWB Hang/Tape/Finish | 5 | 2 | 11-Sep-14 A | 07-Oct-14 | 43 |
| L08-8136 | Install Counter Subtops | 3 | 0 | 11-Sep-14 A | 16-Sep-14 A | |
| L02-6025 | L2 - Framing Go-Back Work (left out for mechanical e | 4 | 0 | 11-Sep-14 A | 02-Oct-14 A | |
| L1-5104a | L1 - Measure/Fabricate Storefront Glazing | 15 | 0 | 12-Sep-14 A | 18-Sep-14 A | |
| L1B-8102c | Finish framing and MEP at Main Ballroom East Wall ( | 10 | 0 | 12-Sep-14 A | 02-Oct-14 A | |
| L09-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L10-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L11-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L12-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L16-7026 | Inspections for GWB Cover | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| MPT-1014 | Tower - Install E/W Wing, N. Side, E. Half (Elev 46-49 | 8 | 5 | 15-Sep-14 A | 22-Oct-14 | 56 |
| LL2-6032 | LL2 - Complete Framing (Including Elevator Lobby) | 4 | 0 | 15-Sep-14 A | 18-Sep-14 A | |
| L1-5104b | L1 - Install Storefront Temporary Enclosures | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| LL1-Z3-FCC18 | FCC - Install Temp Door | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| LL2-2058a | LL2 - GWB Hang 1st Layer | 5 | 0 | 15-Sep-14 A | 19-Sep-14 A | |
| LL2-2064 | LL2 - Generator Room - Finish Exhaust Piping | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| I-3010 | Prepare proposal for MEP relocations | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| L16-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L07-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |

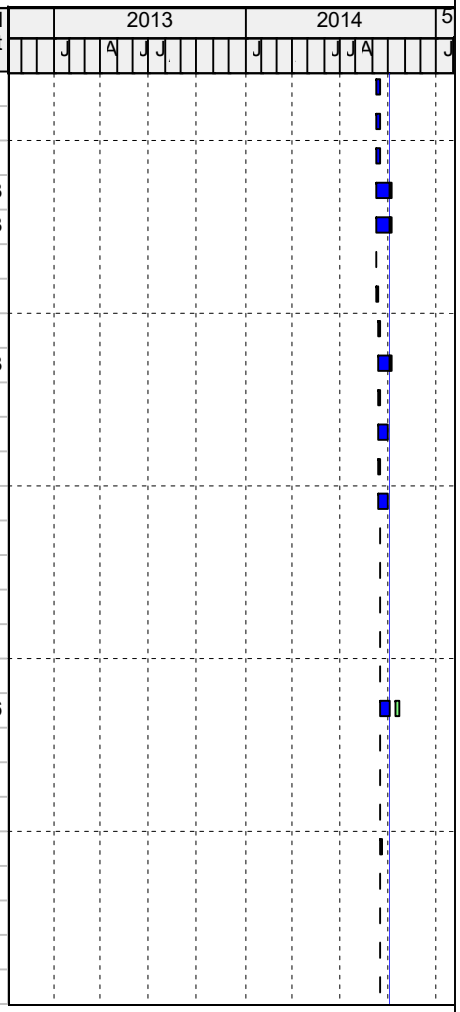



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L10-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L14-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L15-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L03-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| L16-7028 | GWB Hang/Tape/Finish | 5 | 2 | 16-Sep-14 A | 07-Oct-14 | 44 |
| L17-7018 | Electrical Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L09-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L10-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| LL3-6028 | LL3 - Frame Elevator Lobby | 2 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| LL4-6026 | LL4 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| I-3012 | Owner approve proposal for MEP relocations | 3 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| L11-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L12-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L14-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L15-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L04-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L17-7026 | Inspections for GWB Cover | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L17-7116 | Frame Walls | 4 | 0 | 17-Sep-14 A | 29-Sep-14 A | |
| LL2-2066 | LL2 - Generator Room - Finish Fuel Piping | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L16-8395 | Framing at Elevator Lobby | 4 | 0 | 18-Sep-14 A | 26-Sep-14 A | |
| L02-5104 | L2 - Storefront Glazing | 2 | 0 | 18-Sep-14 A | 22-Sep-14 A | |
| L17-7028 | GWB Hang/Tape/Finish | 5 | 2 | 18-Sep-14 A | 07-Oct-14 | 43 |
| LL4-6028 | LL4 - Frame Elevator Lobby | 2 | 0 | 18-Sep-14 A | 02-Oct-14 A | |
| MPT-1010a | Tower - Install E/W Wing, West End (Elev 52,53) | 8 | 1 | 18-Sep-14 A | 06-Oct-14 | 52 |
| LL2-2068 | LL2 - Generator Room - Electrical Finishes | 3 | 0 | 19-Sep-14 A | 30-Sep-14 A | |

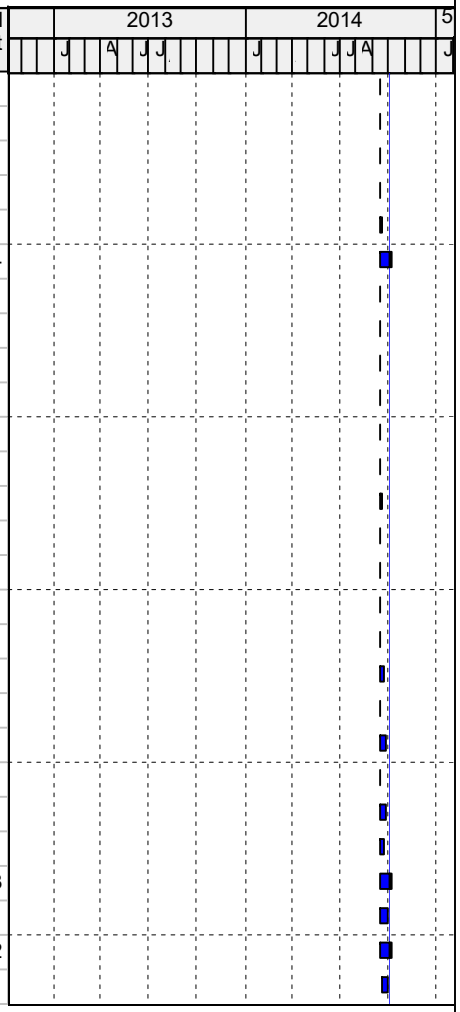



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L09-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L04-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L05-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L03-8140 | Countertops On Site | 0 | 0 | 22-Sep-14 A | | |
| L03-8129a | Shower Doors On Site | 0 | 0 | 22-Sep-14 A | | |
| LL1-Z3-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L1BOH2-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2-2048a | LL2 - Move in Laundry Room Ironer | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2E-8122 | LL2 - Hang GWB at Fire Pump Room | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-FCC20 | FCC - Rough-In and Install Panels | 25 | 15 | 22-Sep-14 A | 24-Oct-14 | 51 |
| I-3014 | Core drill for MEP relocations | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L05-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L07-7028 | GWB Hang/Tape/Finish | 5 | 2 | 23-Sep-14 A | 07-Oct-14 | 43 |
| L09-7028 | GWB Hang/Tape/Finish | 5 | 2 | 23-Sep-14 A | 07-Oct-14 | 43 |
| L14-7028 | GWB Hang/Tape/Finish | 5 | 2 | 23-Sep-14 A | 07-Oct-14 | 43 |
| L04-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L05-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L06-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L07-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L04-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L06-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L04-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |

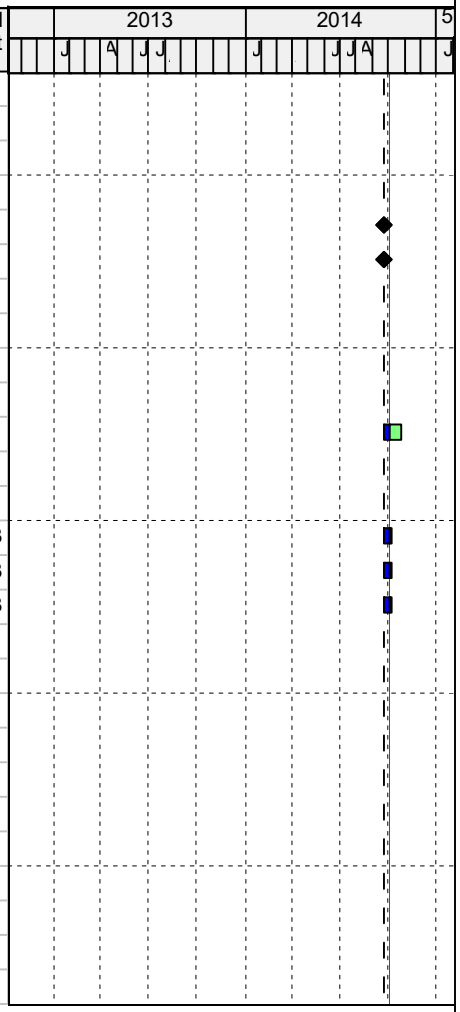



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-7122 | HVAC Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| LL2-2058 | LL2 - Tape/Finish Laundry Room | 3 | 0 | 24-Sep-14 A | 26-Sep-14 A | |
| L08-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L17-8395 | Framing at Elevator Lobby | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L05-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L06-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L07-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L08-7120 | Electrical Rough-In | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| LL2E-8124 | LL2 - Temp-In Louver Opening at Fire Pump Room | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L1-5104c | L1 - Install Storefront at Main Entry Facade | 5 | 2 | 25-Sep-14 A | 07-Oct-14 | 39 |
| L16-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L08-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L10-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L16-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L17-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L17-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L09-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L11-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |

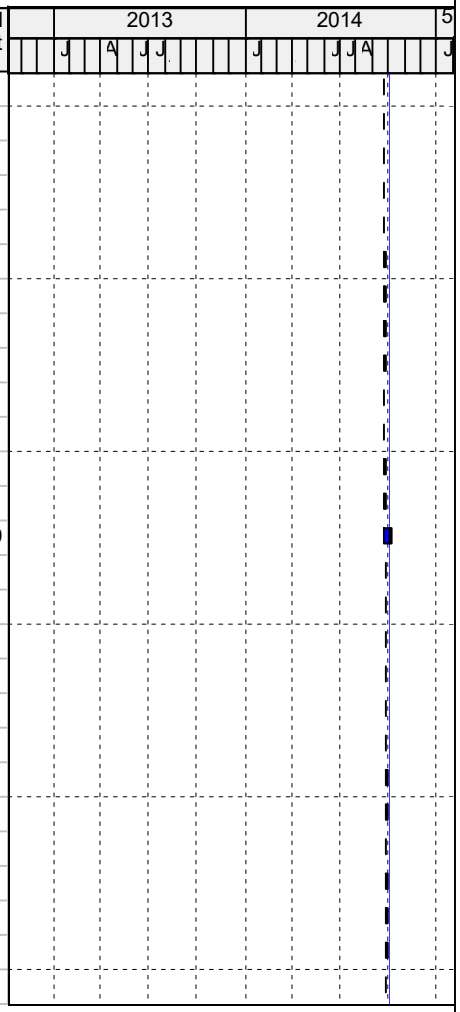



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L14-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L15-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L17-7118 | Install HM Door Frame | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| LL3-6030 | LL3 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL4-6030 | LL4 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL2-6034 | LL2 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L1BOH2-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L02-6030 | L2 - Framing at Elevator Lobby & North Half | 4 | 2 | 29-Sep-14 A | 07-Oct-14 | 25 |
| MPT-1022 | Tower - Caulking, west | 8 | 1 | 29-Sep-14 A | 06-Oct-14 | 52 |
| L17-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L11-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L12-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L07-8121 | Install Bathroom "Barn Doors" | 4 | 1 | 30-Sep-14 A | 08-Oct-14 | 33 |
| L11-8201 | Install ACT Grid @ Corridors | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L09-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L09-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L11-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L12-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L14-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L15-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| LL2-2072 | Generator - Complete generator and annunciator cor | 5 | 1 | 30-Sep-14 A | 06-Oct-14 | 78 |
| L17-6040 | Test Heat Pumps - L16 and L17 | 3 | 1 | 01-Oct-14 A | 06-Oct-14 | 15 |
| L17-6036 | Framing Around Heat Pump & Soffit | 3 | 1 | 01-Oct-14 A | 06-Oct-14 | 17 |
| L14-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |

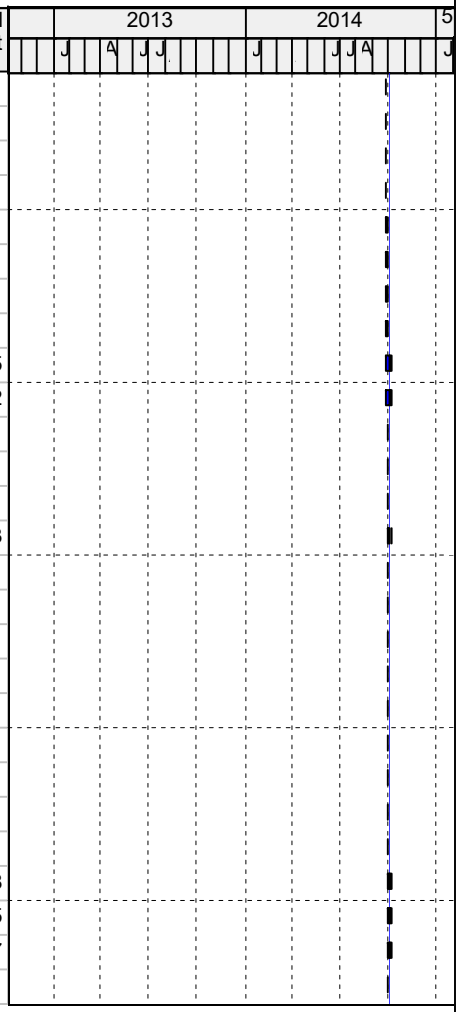



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L11-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L11-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L12-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L12-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L14-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L16-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L17-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L09-8136 | Install Counter Subtops | 3 | 0 | 01-Oct-14 A | 03-Oct-14 A | |
| L02-6032 | L2 - Electrical RI at Elevator Lobby & North Half | 5 | 2 | 01-Oct-14 A | 09-Oct-14 | 25 |
| LL1-Z3-FCC22 | FCC - Finishes | 10 | 7 | 01-Oct-14 A | 14-Oct-14 | 59 |
| L16-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L14-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L15-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1BOH2-8130 | Inspections For Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L02-6024a | L2 - Inspections - South Half | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L16-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| L17-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| LL2-2074 | Generator - Install fuel fill | 2 | 1 | 03-Oct-14 A | 06-Oct-14 | 27 |
| L1BOH2-8100 | Insulation | 4 | 4 | 06-Oct-14 | 09-Oct-14 | 22 |
| LL2-2046 | LL2 - Generator Room - Misc. Finishes | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 60 |
| LL2E-8340 | LL2 - Install walk-in cooler/freezer (BY OTHERS) | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 29 |
| L03-8405 | Cover Inspection | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 33 |

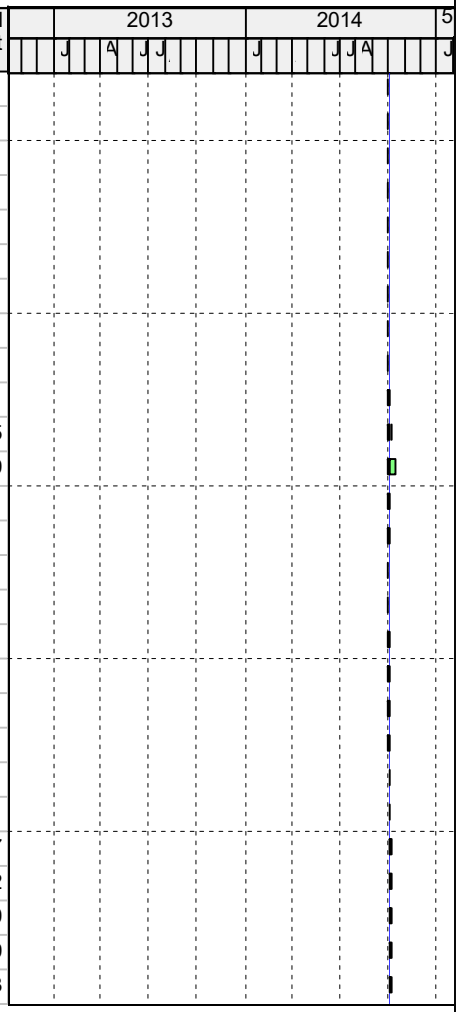



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8405 | Cover Inspection | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 33 |
| L05-8405 | Cover Inspection | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 33 |
| L06-8405 | Cover Inspection | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 35 |
| L07-8405 | Cover Inspection | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 35 |
| L08-8405 | Cover Inspection | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 35 |
| L09-8405 | Cover Inspection | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 37 |
| L10-8405 | Cover Inspection | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 37 |
| L11-8405 | Cover Inspection | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 37 |
| L12-8405 | Cover Inspection | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 39 |
| L14-8405 | Cover Inspection | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 39 |
| L15-8405 | Cover Inspection | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 39 |
| L16-8405 | Cover Inspection | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 41 |
| L17-8405 | Cover Inspection | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 41 |
| RF-4008 | Tower Roof - Install corrugated metal panels | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 40 |
| L06-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 06-Oct-14 | 09-Oct-14 | 39 |
| L03-7128 | Inspections for GWB Cover | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 42 |
| L04-7030 | Paint | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 45 |
| L05-7030 | Paint | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 48 |
| L04-7128 | Inspections for GWB Cover | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 43 |
| L05-7128 | Inspections for GWB Cover | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 43 |
| L06-7128 | Inspections for GWB Cover | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 43 |
| L07-7128 | Inspections for GWB Cover | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 43 |
| L08-7128 | Inspections for GWB Cover | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 43 |
| L09-7128 | Inspections for GWB Cover | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 43 |
| L10-7128 | Inspections for GWB Cover | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 43 |
| L11-7128 | Inspections for GWB Cover | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 43 |
| L12-7128 | Inspections for GWB Cover | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 43 |

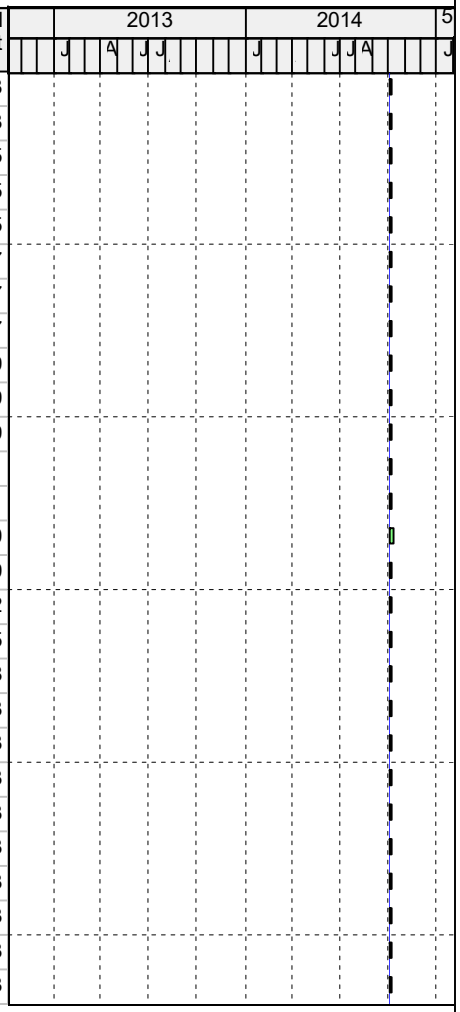



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-7128 | Inspections for GWB Cover | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 45 |
| L15-7128 | Inspections for GWB Cover | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 43 |
| L16-7128 | Inspections for GWB Cover | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 44 |
| L17-7128 | Inspections for GWB Cover | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 43 |
| MPT-1016 | Tower - Install N/S Wing, S. End W. of Manlift (Elev 2 | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 69 |
| MPT-1020 | Tower - Install E/W Wing, East End (Elev 41,44) | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 52 |
| L10-8136 | Install Counter Subtops | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 29 |
| LL1-Z3-6032 | GWB Hang/Tape at Elevator Lobby | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 38 |
| LL2-2060 | LL2 - Paint Prime/First Coat at Laundry Room | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 53 |
| L03-8200a | New murals on site (date estimated) | 0 | 0 | 06-Oct-14* | | 42 |
| L03-8200b | Install Guestroom Murals | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 42 |
| MPT-1018b | Tower - Roof cornice frame & sheath | 6 | 6 | 06-Oct-14 | 13-Oct-14 | 52 |
| L02-8100a | L2 - Insulation - South Half | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 37 |
| L02-8102a | L2 - GWB Hang / Tape / Finish - South Half | 7 | 7 | 06-Oct-14 | 14-Oct-14 | 37 |
| SW-2102 | Zone 1 - Vacate SE corner | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 28 |
| SW-2100 | Zone 1 - Survey | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 30 |
| SW-2104 | Zone 1 - Install lighting conduit at SE corner | 7 | 7 | 06-Oct-14 | 14-Oct-14 | 30 |
| PC-4012 | Porte Cochere - Install sheet metal capping | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 73 |
| RF-4048 | Tower Roof - Install davit arms | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 41 |
| L1BOH2-8102 | GWB Hang (Walls) | 5 | 5 | 07-Oct-14 | 11-Oct-14 | 26 |
| L17-6038 | Electrical at Heat Pump & Soffit | 1 | 1 | 07-Oct-14 | 07-Oct-14 | 17 |
| L03-8404 | GWB Hang/Tape Finish at Elevator Lobby | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 33 |
| L04-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 33 |
| L05-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 33 |
| LL2E-8342 | LL2 - Final connections at walk-in cooler/freezer | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 39 |
| L03-7130 | GWB Hang/Tape/Finish | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 42 |
| L04-7032 | Install VCT Flooring (x42) | 1 | 1 | 07-Oct-14 | 07-Oct-14 | 45 |

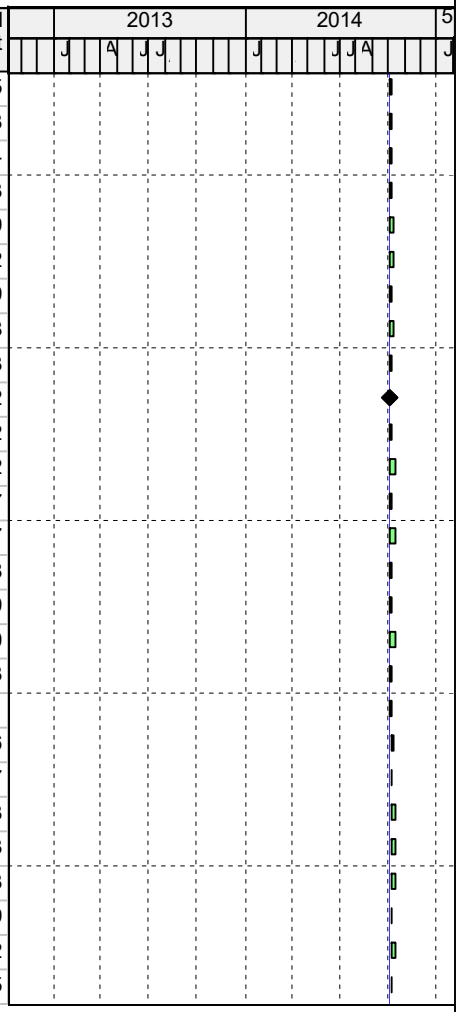



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7032 | Install VCT Flooring (x42) | 1 | 1 | 07-Oct-14 | 07-Oct-14 | 48 |
| L04-7130 | GWB Hang/Tape/Finish | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 43 |
| L05-7130 | GWB Hang/Tape/Finish | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 43 |
| SW-2200 | Zone 2 - Sawcut asphalt | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 31 |
| SW-2300 | Zone 3 - Sawcut asphalt | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 31 |
| SW-2106 | Zone 1 - Sawcut and remove asphalt | 2 | 2 | 07-Oct-14 | 08-Oct-14 | 30 |
| SW-2108 | Zone 1 - Install east footing drain | 4 | 4 | 07-Oct-14 | 10-Oct-14 | 28 |
| MPT-1024 | Tower - Caulking, east | 9 | 9 | 07-Oct-14 | 17-Oct-14 | 52 |
| LL2-2076 | Generator - Install fuel fill mechanical piping | 4 | 4 | 07-Oct-14 | 10-Oct-14 | 27 |
| LL2-2048 | LL2 - Set Laundry Room equipment (BY OTHERS) | 3 | 3 | 08-Oct-14 | 10-Oct-14 | 53 |
| L03-8129 | Install Shower Doors | 4 | 4 | 08-Oct-14 | 13-Oct-14 | 29 |
| L03-7030 | Paint | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 43 |
| L04-7034 | Install Door and Hardware (x42) | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 45 |
| L05-7034 | Install Door and Hardware (x42) | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 48 |
| L06-7030 | Paint | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 43 |
| L07-7030 | Paint | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 43 |
| L08-7030 | Paint | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 43 |
| L09-7030 | Paint | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 43 |
| L10-7030 | Paint | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 43 |
| L11-7030 | Paint | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 43 |
| L12-7030 | Paint | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 43 |
| L14-7030 | Paint | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 43 |
| L15-7030 | Paint | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 43 |
| L16-7030 | Paint | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 44 |
| L17-7030 | Paint | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 43 |
| L03-8138 | Install Toilet Accessories | 4 | 4 | 08-Oct-14 | 13-Oct-14 | 26 |
| L04-8200a | Install Guestroom Murals | 2 | 2 | 08-Oct-14 | 09-Oct-14 | 42 |

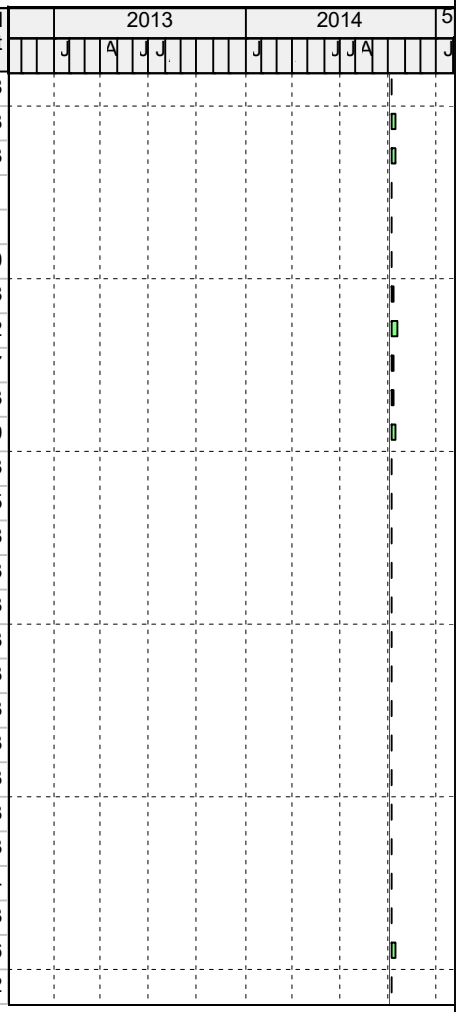



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8633 | Pool - Install waterproofing | 3 | 3 | 08-Oct-14* | 10-Oct-14 | 9 |
| CO-7204 | Cx - Gas Service established | 0 | 0 | | 08-Oct-14* | 6 |
| L06-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 33 |
| L07-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 33 |
| L08-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 33 |
| L08-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 09-Oct-14 | 14-Oct-14 | 32 |
| L03-7032 | Install VCT Flooring (x42) | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 43 |
| L04-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 09-Oct-14 | 13-Oct-14 | 45 |
| L05-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 09-Oct-14 | 13-Oct-14 | 48 |
| L06-7032 | Install VCT Flooring (x42) | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 43 |
| L07-7032 | Install VCT Flooring (x42) | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 43 |
| L08-7032 | Install VCT Flooring (x42) | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 43 |
| L09-7032 | Install VCT Flooring (x42) | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 43 |
| L10-7032 | Install VCT Flooring (x42) | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 43 |
| L11-7032 | Install VCT Flooring (x42) | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 43 |
| L12-7032 | Install VCT Flooring (x42) | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 43 |
| L14-7032 | Install VCT Flooring (x42) | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 43 |
| L15-7032 | Install VCT Flooring (x42) | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 43 |
| L16-7032 | Install VCT Flooring (x42) | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 44 |
| L17-7032 | Install VCT Flooring (x42) | 1 | 1 | 09-Oct-14 | 09-Oct-14 | 43 |
| L06-7130 | GWB Hang/Tape/Finish | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 41 |
| L07-7130 | GWB Hang/Tape/Finish | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 41 |
| L08-7130 | GWB Hang/Tape/Finish | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 41 |
| L11-8136 | Install Counter Subtops | 3 | 3 | 09-Oct-14 | 13-Oct-14 | 29 |
| LL1-Z2-8102a | GWB Hang (Ceilings) & Inspection | 9 | 9 | 09-Oct-14 | 21-Oct-14 | 19 |
| SW-2110 | Zone 1 - Adjust utilities structures | 2 | 2 | 09-Oct-14 | 10-Oct-14 | 30 |
| SW-2109 | Zone 1 - Install irrigation sleeves | 2 | 2 | 09-Oct-14 | 10-Oct-14 | 42 |

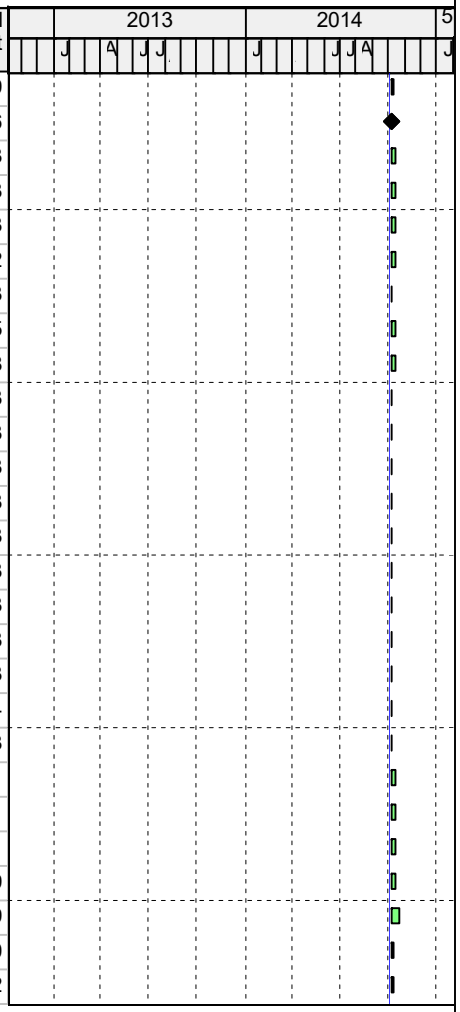



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7206 | Cx - Purge/Prove Gas-Fed Equipment and Feeder Li | 7 | 7 | 09-Oct-14 | 17-Oct-14 | 6 |
| L04-8129 | Install Shower Doors | 4 | 4 | 10-Oct-14 | 15-Oct-14 | 29 |
| L03-7034 | Install Door and Hardware (x42) | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 43 |
| L06-7034 | Install Door and Hardware (x42) | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 43 |
| L07-7034 | Install Door and Hardware (x42) | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 43 |
| L08-7034 | Install Door and Hardware (x42) | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 43 |
| L09-7034 | Install Door and Hardware (x42) | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 43 |
| L10-7034 | Install Door and Hardware (x42) | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 43 |
| L11-7034 | Install Door and Hardware (x42) | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 43 |
| L12-7034 | Install Door and Hardware (x42) | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 43 |
| L14-7034 | Install Door and Hardware (x42) | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 43 |
| L15-7034 | Install Door and Hardware (x42) | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 43 |
| L16-7034 | Install Door and Hardware (x42) | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 44 |
| L17-7034 | Install Door and Hardware (x42) | 1 | 1 | 10-Oct-14 | 10-Oct-14 | 43 |
| L04-8138 | Install Toilet Accessories | 4 | 4 | 10-Oct-14 | 14-Oct-14 | 31 |
| L1K-8102a | GWB Hang (Ceilings at Public Restroom) & Inspectio | 4 | 4 | 10-Oct-14 | 15-Oct-14 | 17 |
| L05-8200a | Install Guestroom Murals | 2 | 2 | 10-Oct-14 | 13-Oct-14 | 42 |
| SW-2112 | Zone 1 - Grade for curb and gutter | 3 | 3 | 10-Oct-14 | 14-Oct-14 | 28 |
| RF-4046 | Tower Roof - Install sheet metal capping | 6 | 6 | 10-Oct-14 | 17-Oct-14 | 40 |
| ML-5962 | Man/Material Lifts - Remove Roof Lift Stop | 0 | 0 | | 11-Oct-14* | 80 |
| L1BOH2-8215 | GWB Tape (Walls) | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 22 |
| L09-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 33 |
| L10-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 33 |
| L11-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 33 |
| LL2-2050 | LL2 - Laundry Room equipment final connections (M | 4 | 4 | 13-Oct-14 | 16-Oct-14 | 53 |
| LL1-6014lb | L1 bar redesign - rework ceiling framing & inspection | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 19 |
| L03-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 43 |

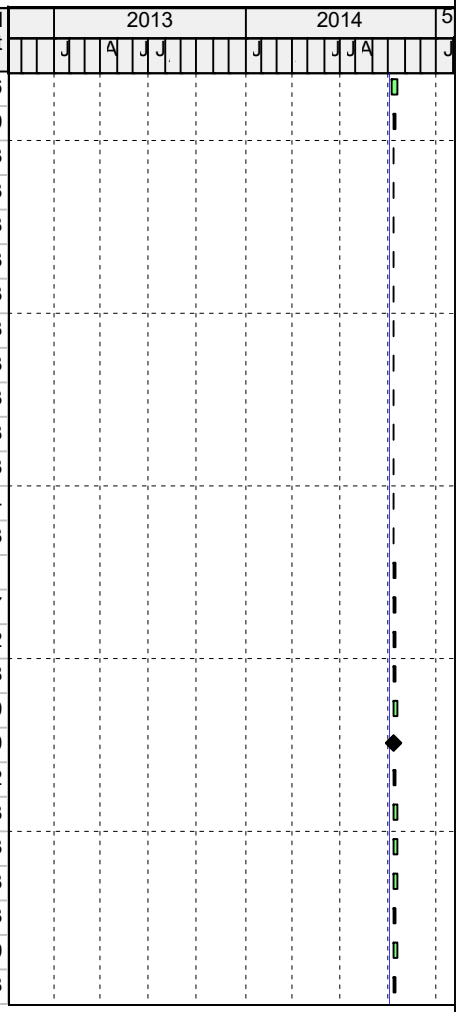



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 43 |
| L07-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 43 |
| L08-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 43 |
| L09-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 43 |
| L10-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 43 |
| L11-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 43 |
| L12-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 43 |
| L14-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 43 |
| L15-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 43 |
| L16-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 44 |
| L17-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 43 |
| L09-7130 | GWB Hang/Tape/Finish | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 39 |
| L10-7130 | GWB Hang/Tape/Finish | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 39 |
| L11-7130 | GWB Hang/Tape/Finish | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 39 |
| L05-8138 | Install Toilet Accessories | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 26 |
| LL4-8102a | LL4 - GWB Tape/Finish | 4 | 4 | 13-Oct-14 | 16-Oct-14 | 42 |
| LL3-8102a | LL3 - GWB Tape/Finish | 4 | 4 | 13-Oct-14 | 16-Oct-14 | 42 |
| L1B-8102b | GWB Hang (Walls) & Inspection - Exterior Wall at Cor | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 2 |
| SW-2202 | Zone 2 - Install lighting conduit | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 29 |
| SW-2204 | Zone 2 - Repave utility trenches | 4 | 4 | 13-Oct-14 | 16-Oct-14 | 29 |
| RF-4050 | Roof at Manlift - Erect steel | 1 | 1 | 13-Oct-14 | 13-Oct-14 | 53 |
| MPT-1030 | Tower - Install sign backing NE (Elev 44) | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 60 |
| LL2-2078 | Generator - Install fuel fill control wiring | 2 | 2 | 13-Oct-14 | 14-Oct-14 | 27 |
| LL2-2080 | Generator - Complete generator accessories (battery) | 1 | 1 | 13-Oct-14 | 13-Oct-14 | 31 |
| L03-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 14-Oct-14 | 16-Oct-14 | 40 |
| L04-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 14-Oct-14 | 16-Oct-14 | 41 |
| L05-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 14-Oct-14 | 16-Oct-14 | 41 |

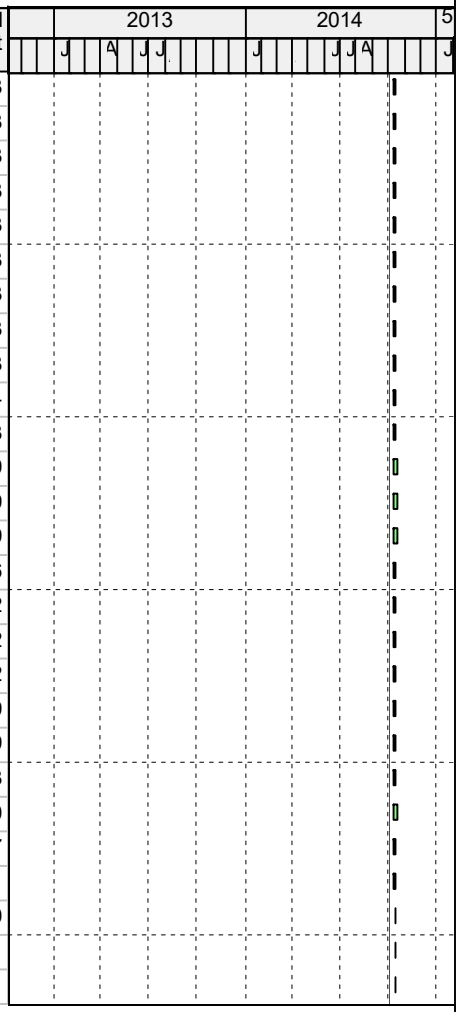



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8129 | Install Shower Doors | 4 | 4 | 14-Oct-14 | 17-Oct-14 | 29 |
| L12-8201 | Install ACT Grid @ Corridors | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 48 |
| L03-7132 | Paint Prime/1st Coat | 3 | 3 | 14-Oct-14 | 16-Oct-14 | 42 |
| L04-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 45 |
| L05-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 48 |
| L04-7132 | Paint Prime/1st Coat | 3 | 3 | 14-Oct-14 | 16-Oct-14 | 43 |
| L05-7132 | Paint Prime/1st Coat | 3 | 3 | 14-Oct-14 | 16-Oct-14 | 43 |
| L12-8136 | Install Counter Subtops | 3 | 3 | 14-Oct-14 | 16-Oct-14 | 29 |
| L02-6016a | L2 - Electrical Room Buildout | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 52 |
| L06-8200a | Install Guestroom Murals | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 42 |
| SW-2203 | Zone 2 - Install irrigation sleeves | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 40 |
| SW-2302 | Zone 3 - Grade for curb and gutter | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 28 |
| RF-4052 | Roof at Manlift - Framing/sheathing/air barrier (inspec | 4 | 4 | 14-Oct-14 | 17-Oct-14 | 53 |
| L12-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 33 |
| L14-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 33 |
| L15-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 33 |
| L12-7130 | GWB Hang/Tape/Finish | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 37 |
| L14-7130 | GWB Hang/Tape/Finish | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 39 |
| L15-7130 | GWB Hang/Tape/Finish | 5 | 5 | 15-Oct-14 | 21-Oct-14 | 37 |
| LL2-8106a | LL2 - Pinned Insulation @ Ramp Ceiling | 4 | 4 | 15-Oct-14 | 20-Oct-14 | 39 |
| L02-8104a | L2 - Int Painting - South Half | 2 | 2 | 15-Oct-14 | 16-Oct-14 | 37 |
| SW-2114 | Zone 1 - FRP curb and gutter | 3 | 3 | 15-Oct-14 | 17-Oct-14 | 30 |
| L1BOH2-8104 | Prime Paint | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 26 |
| I-1102 | Additional work at new L17 guest rooms | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 15 |
| L06-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 16-Oct-14 | 20-Oct-14 | 39 |
| L07-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 16-Oct-14 | 20-Oct-14 | 39 |
| L08-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 16-Oct-14 | 20-Oct-14 | 39 |

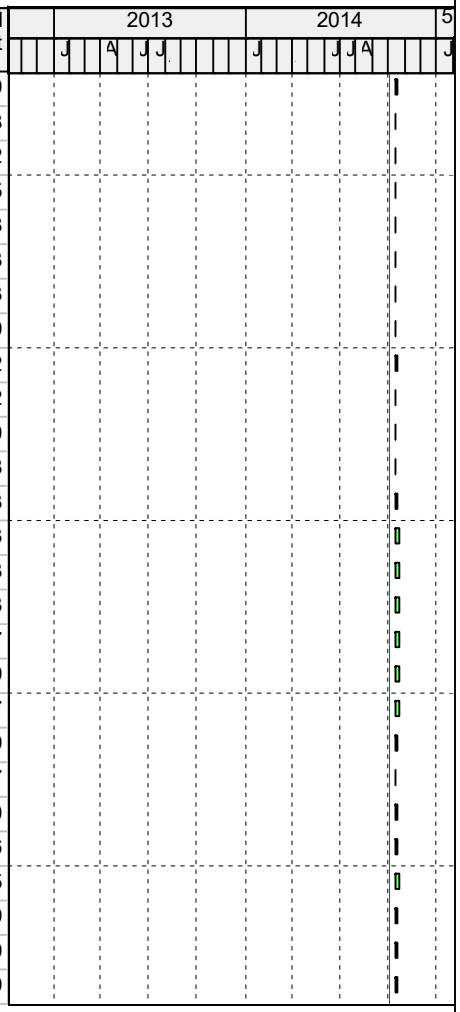



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8129 | Install Shower Doors | 4 | 4 | 16-Oct-14 | 21-Oct-14 | 29 |
| L14-8201 | Install ACT Grid @ Corridors | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 46 |
| L03-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 43 |
| L04-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 45 |
| L05-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 48 |
| L06-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 43 |
| L07-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 43 |
| L08-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 43 |
| L09-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 43 |
| L10-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 43 |
| L11-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 43 |
| L12-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 43 |
| L14-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 43 |
| L15-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 43 |
| L16-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 44 |
| L17-7038 | Electrical Terminations & Trim-Out | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 43 |
| L06-7132 | Paint Prime/1st Coat | 3 | 3 | 16-Oct-14 | 20-Oct-14 | 41 |
| L07-7132 | Paint Prime/1st Coat | 3 | 3 | 16-Oct-14 | 20-Oct-14 | 41 |
| L08-7132 | Paint Prime/1st Coat | 3 | 3 | 16-Oct-14 | 20-Oct-14 | 41 |
| L03-8634 | Pool - Install reinforcing steel & inspect | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 9 |
| MPT-1018 | Tower - Install Roof Penthouse (Elev 36b,37,38.39) | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 44 |
| L06-8138 | Install Toilet Accessories | 4 | 4 | 16-Oct-14 | 21-Oct-14 | 25 |
| LL2-2062 | LL2 - Connect Eye Wash and Sinks at Laundry Roon | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 53 |
| L07-8200a | Install Guestroom Murals | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 42 |
| L1B-8102d | GWB Hang (Walls) & Inspection - Main Ballroom East | 1 | 1 | 16-Oct-14 | 16-Oct-14 | 2 |
| SW-2116 | Zone 1 - Fine grade for sidewalk | 4 | 4 | 16-Oct-14 | 21-Oct-14 | 39 |
| SW-2206 | Zone 2 - Grade for curb and gutter | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 28 |

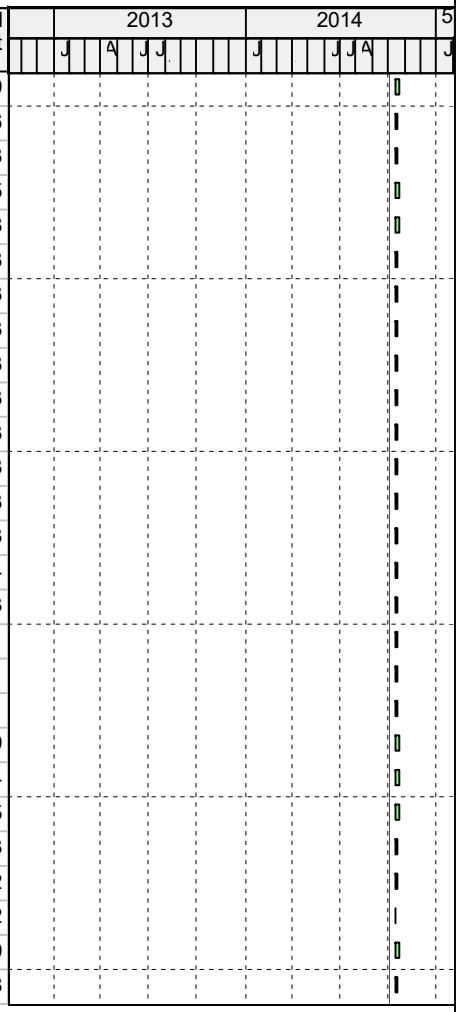



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2304 | Zone 3 - FRP curb and gutter | 3 | 3 | 16-Oct-14 | 20-Oct-14 | 29 |
| LL2-2082 | Generator - Cx fuel fill | 1 | 1 | 16-Oct-14 | 16-Oct-14 | 27 |
| L1BOH2-8114 | T Bar Grid Ceiling | 3 | 3 | 17-Oct-14 | 21-Oct-14 | 21 |
| L03-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 17-Oct-14 | 20-Oct-14 | 40 |
| L04-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 17-Oct-14 | 20-Oct-14 | 41 |
| L05-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 17-Oct-14 | 20-Oct-14 | 41 |
| L16-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 33 |
| L17-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 33 |
| L09-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 17-Oct-14 | 22-Oct-14 | 28 |
| L16-7130 | GWB Hang/Tape/Finish | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 36 |
| L17-7130 | GWB Hang/Tape/Finish | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 35 |
| L14-8136 | Install Counter Subtops | 3 | 3 | 17-Oct-14 | 21-Oct-14 | 29 |
| LL1-8102a | GWB Hang/Tape (Ceilings) | 10 | 10 | 17-Oct-14 | 28-Oct-14 | 23 |
| LL2-2084 | Generator - Initial fuel fill | 1 | 1 | 17-Oct-14 | 17-Oct-14 | 27 |
| LL2-2070 | LL2 - Generator Room - Generator Ready for Startup | 0 | 0 | | 17-Oct-14 | 27 |
| CO-7200 | Cx - Penthouse Mechanical Installation Complete | 0 | 0 | | 17-Oct-14 | 4 |
| CO-7202 | Cx - Electrical Internal Bus & LL2-L17 Bus Duct Energ | 0 | 0 | | 17-Oct-14 | 4 |
| L09-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 37 |
| L10-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 37 |
| L11-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 37 |
| MPP-1004 | Podium - Pool Area & Cornice | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 44 |
| MPP-1006 | Podium - Install Level 3 Cornice (All 4 Sides) | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 44 |
| MPP-1010 | Podium - Install East Elevation (Elev 5 & 7) | 7 | 7 | 20-Oct-14 | 28-Oct-14 | 44 |
| L07-8129 | Install Shower Doors | 4 | 4 | 20-Oct-14 | 23-Oct-14 | 29 |
| L15-8201 | Install ACT Grid @ Corridors | 2 | 2 | 20-Oct-14 | 21-Oct-14 | 44 |
| L03-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 43 |
| L06-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 43 |

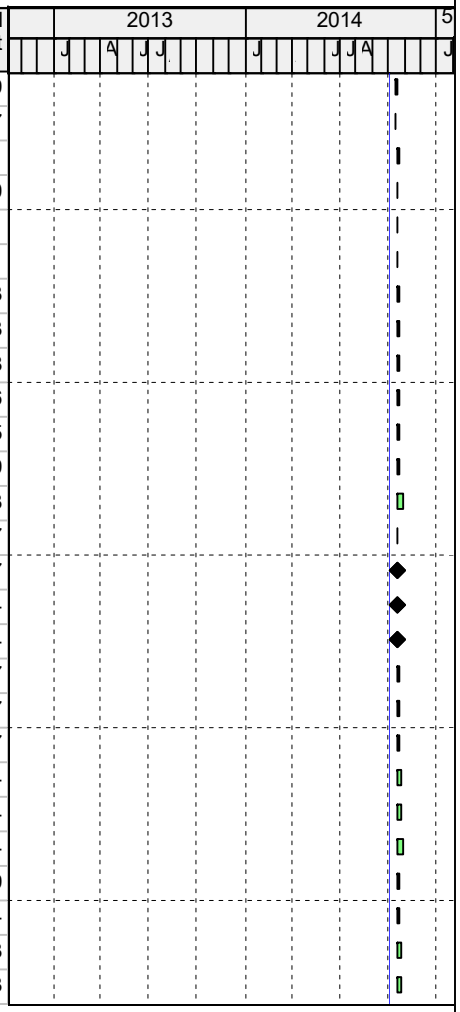



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 43 |
| L08-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 43 |
| L09-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 43 |
| L10-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 43 |
| L11-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 43 |
| L12-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 43 |
| L14-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 43 |
| L15-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 43 |
| L16-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 44 |
| L17-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 43 |
| L09-7132 | Paint Prime/1st Coat | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 39 |
| L10-7132 | Paint Prime/1st Coat | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 39 |
| L11-7132 | Paint Prime/1st Coat | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 39 |
| L07-8138 | Install Toilet Accessories | 4 | 4 | 20-Oct-14 | 23-Oct-14 | 25 |
| LL1-6014lb2 | L1 bar redesign - GWB hang at ceilings | 4 | 4 | 20-Oct-14 | 23-Oct-14 | 19 |
| L08-8200a | Install Guestroom Murals | 2 | 2 | 20-Oct-14 | 21-Oct-14 | 42 |
| SW-2208 | Zone 2 - FRP curb and gutter | 2 | 2 | 20-Oct-14 | 21-Oct-14 | 28 |
| RF-4044 | Ballroom Roof - Install sheet metal capping | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 40 |
| RF-4054 | Roof at Manlift - Final mechanical installations | 4 | 4 | 20-Oct-14 | 23-Oct-14 | 53 |
| MPT-1026 | Tower - Caulking, north | 10 | 10 | 20-Oct-14 | 31-Oct-14 | 52 |
| MPT-1032 | Tower - Install sign backing NW (Elev 51,52) | 4 | 4 | 20-Oct-14 | 23-Oct-14 | 60 |
| CO-7158 | Generator - Interim electrical inspection | 1 | 1 | 20-Oct-14 | 20-Oct-14 | 27 |
| CO-7208 | Cx - Start-Up Pumps | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 4 |
| CO-7210 | Cx - Start-Up VFD's | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 4 |
| CO-7212 | Cx - Start-Up Boilers | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 6 |
| L03-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 40 |
| L03-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 21-Oct-14 | 21-Oct-14 | 42 |

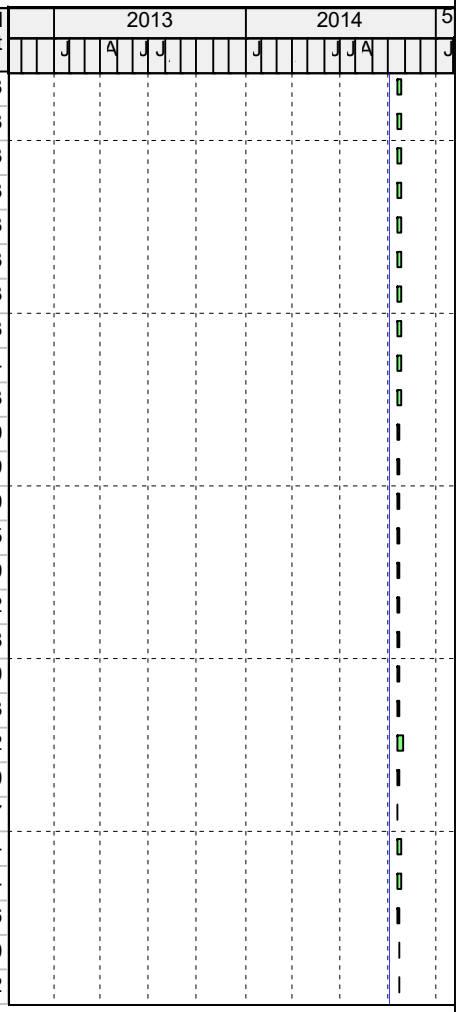



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 41 |
| L04-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 21-Oct-14 | 21-Oct-14 | 42 |
| L05-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 41 |
| L05-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 21-Oct-14 | 21-Oct-14 | 43 |
| L06-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 21-Oct-14 | 22-Oct-14 | 39 |
| L07-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 21-Oct-14 | 22-Oct-14 | 39 |
| L08-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 21-Oct-14 | 22-Oct-14 | 39 |
| L10-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 21-Oct-14 | 24-Oct-14 | 28 |
| L03-7138 | Electrical Trim-Out | 2 | 2 | 21-Oct-14 | 22-Oct-14 | 40 |
| L03-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 40 |
| L04-7138 | Electrical Trim-Out | 2 | 2 | 21-Oct-14 | 22-Oct-14 | 41 |
| L04-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 41 |
| L05-7138 | Electrical Trim-Out | 2 | 2 | 21-Oct-14 | 22-Oct-14 | 41 |
| L05-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 41 |
| L03-7144 | Fire Sprinkler Trim | 1 | 1 | 21-Oct-14 | 21-Oct-14 | 42 |
| L04-7144 | Fire Sprinkler Trim | 1 | 1 | 21-Oct-14 | 21-Oct-14 | 43 |
| L05-7144 | Fire Sprinkler Trim | 1 | 1 | 21-Oct-14 | 21-Oct-14 | 43 |
| CO-7160 | Generator - Cx generator/owner training | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 27 |
| L12-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 35 |
| L14-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 35 |
| L15-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 35 |
| L08-8129 | Install Shower Doors | 4 | 4 | 22-Oct-14 | 27-Oct-14 | 29 |
| L12-7132 | Paint Prime/1st Coat | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 37 |
| L14-7132 | Paint Prime/1st Coat | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 39 |
| L15-7132 | Paint Prime/1st Coat | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 37 |
| L08-8138 | Install Toilet Accessories | 4 | 4 | 22-Oct-14 | 27-Oct-14 | 25 |
| L15-8136 | Install Counter Subtops | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 29 |

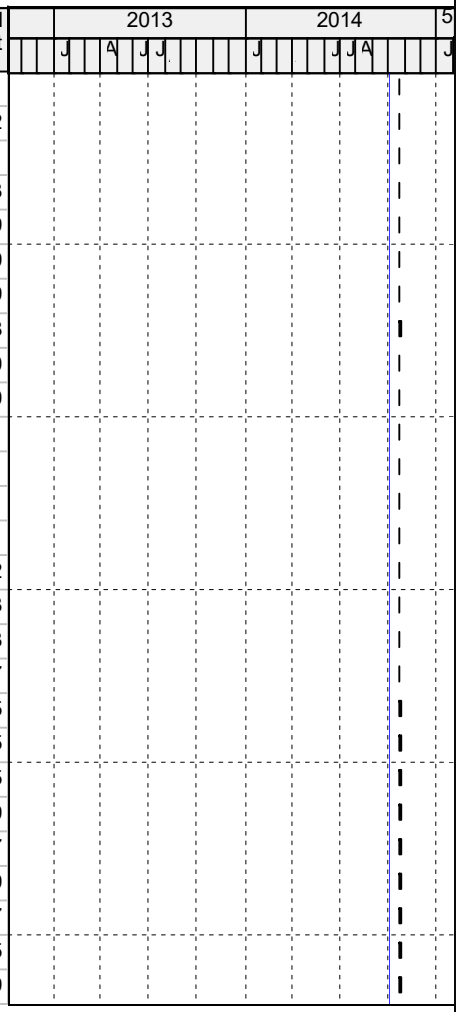



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1BOH2C-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 21 |
| L1BOH2C-6014 | Complete Plumbing RI @ Ceilings & Inspection | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 21 |
| L1BOH2C-6016 | Complete Electrical RI @ Ceilings & Inspection | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 21 |
| L1BOH2C-6018 | Complete HVAC RI @ Ceilings & Inspection | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 21 |
| L1BOH2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 21 |
| SW-2118 | Zone 1 - FRP sidewalk | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 39 |
| SW-2210 | Zone 2 - Fine grade for sidewalk | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 36 |
| SW-2306 | Prep, grind and overlay at 11th Ave, 3rd Place & 2nd | 8 | 8 | 22-Oct-14 | 31-Oct-14 | 28 |
| RF-4042 | Pool Roof - Install sheet metal capping | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 40 |
| RF-4056 | Roof at Manlift - Final electrical connections | 2 | 2 | 22-Oct-14 | 23-Oct-14 | 53 |
| L04-8418 | Flooring at Elevator Lobby | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 41 |
| L06-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 39 |
| L06-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 23-Oct-14 | 23-Oct-14 | 41 |
| L07-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 39 |
| L07-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 23-Oct-14 | 23-Oct-14 | 41 |
| L08-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 39 |
| L08-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 23-Oct-14 | 23-Oct-14 | 41 |
| L09-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 37 |
| L10-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 37 |
| L11-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 37 |
| L11-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 23-Oct-14 | 28-Oct-14 | 28 |
| L04-7042 | Install Tile Flooring (x41) | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 45 |
| L05-7042 | Install Tile Flooring (x41) | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 48 |
| L06-7138 | Electrical Trim-Out | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 39 |
| L06-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 39 |
| L07-7138 | Electrical Trim-Out | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 39 |
| L07-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 39 |

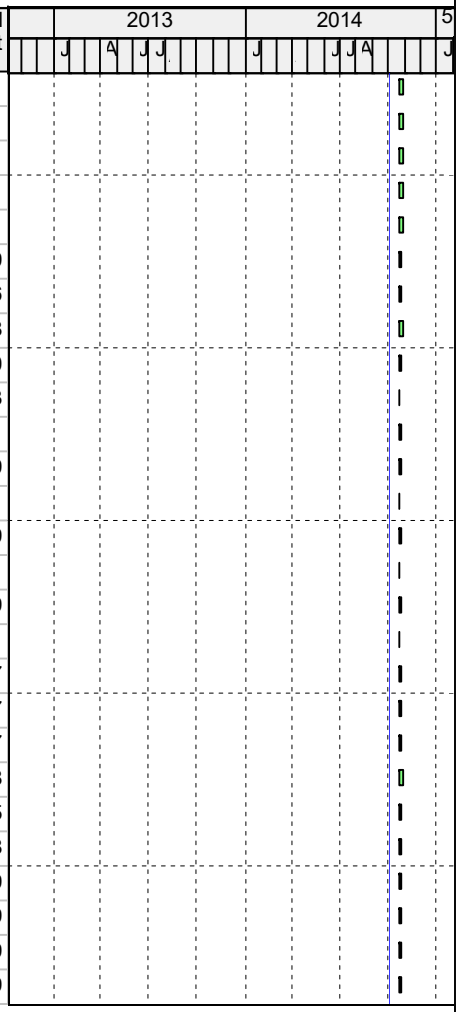



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7138 | Electrical Trim-Out | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 39 |
| L08-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 39 |
| L03-8636 | Pool - Shotcrete | 1 | 1 | 23-Oct-14 | 23-Oct-14 | 9 |
| L16-8136 | Install Counter Subtops | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 31 |
| L04-8206a | Install Base @ Corridors | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 45 |
| MPT-1018a | Tower - Install Roof Cornice Metal | 5 | 5 | 23-Oct-14 | 29-Oct-14 | 56 |
| L06-7144 | Fire Sprinkler Trim | 1 | 1 | 23-Oct-14 | 23-Oct-14 | 41 |
| L07-7144 | Fire Sprinkler Trim | 1 | 1 | 23-Oct-14 | 23-Oct-14 | 41 |
| L08-7144 | Fire Sprinkler Trim | 1 | 1 | 23-Oct-14 | 23-Oct-14 | 41 |
| L03-8418 | Flooring at Elevator Lobby | 3 | 3 | 24-Oct-14 | 28-Oct-14 | 40 |
| L05-8418 | Flooring at Elevator Lobby | 3 | 3 | 24-Oct-14 | 28-Oct-14 | 41 |
| L16-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Oct-14 | 28-Oct-14 | 34 |
| L17-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Oct-14 | 28-Oct-14 | 33 |
| L09-8129 | Install Shower Doors | 4 | 4 | 24-Oct-14 | 28-Oct-14 | 35 |
| L03-7134 | Install VCT Flooring & Base | 3 | 3 | 24-Oct-14 | 28-Oct-14 | 40 |
| L04-7134 | Install VCT Flooring | 3 | 3 | 24-Oct-14 | 28-Oct-14 | 41 |
| L05-7134 | Install VCT Flooring | 3 | 3 | 24-Oct-14 | 28-Oct-14 | 41 |
| L16-7132 | Paint Prime/1st Coat | 3 | 3 | 24-Oct-14 | 28-Oct-14 | 36 |
| L17-7132 | Paint Prime/1st Coat | 3 | 3 | 24-Oct-14 | 28-Oct-14 | 35 |
| L05-8206a | Install Base @ Corridors | 3 | 3 | 24-Oct-14 | 28-Oct-14 | 44 |
| SW-2214 | Zone 2 - Adjust utilities structures | 2 | 2 | 24-Oct-14 | 27-Oct-14 | 38 |
| RF-4058 | Roof at Manlift - Install roofing | 2 | 2 | 24-Oct-14 | 27-Oct-14 | 53 |
| CO-7162 | Generator - Load bank testing | 1 | 1 | 24-Oct-14 | 24-Oct-14 | 27 |
| L09-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 27-Oct-14 | 29-Oct-14 | 37 |
| L09-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 27-Oct-14 | 27-Oct-14 | 39 |
| L10-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 27-Oct-14 | 29-Oct-14 | 37 |
| L10-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 27-Oct-14 | 27-Oct-14 | 39 |

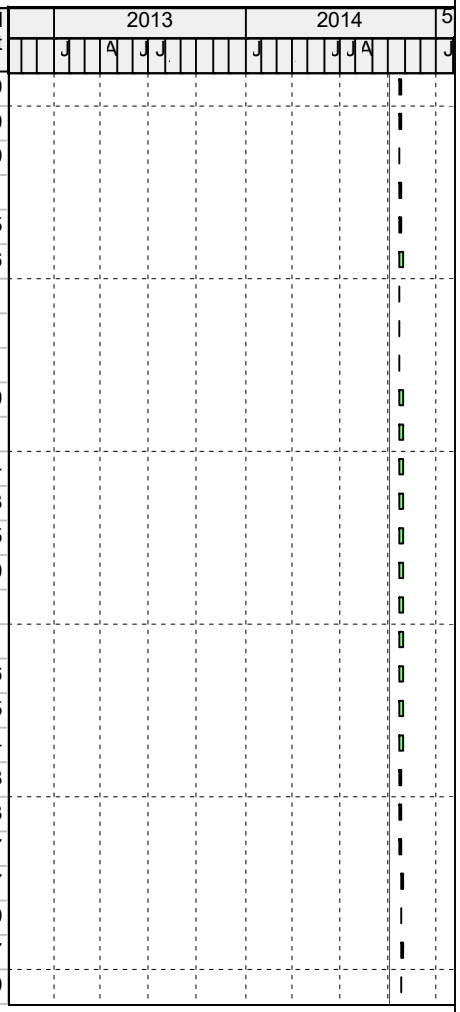



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 27-Oct-14 | 29-Oct-14 | 37 |
| L11-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 27-Oct-14 | 27-Oct-14 | 39 |
| L12-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 35 |
| L14-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 35 |
| L15-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 35 |
| MPP-1000 | Podium - Install W/S/N Elevations (Elev 1-5, 6,9-19,2 | 10 | 10 | 27-Oct-14 | 07-Nov-14 | 44 |
| L12-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 27-Oct-14 | 30-Oct-14 | 28 |
| L03-7042 | Install Tile Flooring (x41) | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 43 |
| L04-7044 | Install Vending Cabinets (x41) | 1 | 1 | 27-Oct-14 | 27-Oct-14 | 45 |
| L05-7044 | Install Vending Cabinets (x41) | 1 | 1 | 27-Oct-14 | 27-Oct-14 | 52 |
| L06-7042 | Install Tile Flooring (x41) | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 43 |
| L07-7042 | Install Tile Flooring (x41) | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 43 |
| L08-7042 | Install Tile Flooring (x41) | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 43 |
| L09-7042 | Install Tile Flooring (x41) | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 43 |
| L10-7042 | Install Tile Flooring (x41) | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 43 |
| L11-7042 | Install Tile Flooring (x41) | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 43 |
| L12-7042 | Install Tile Flooring (x41) | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 43 |
| L14-7042 | Install Tile Flooring (x41) | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 43 |
| L15-7042 | Install Tile Flooring (x41) | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 43 |
| L16-7042 | Install Tile Flooring (x41) | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 44 |
| L17-7042 | Install Tile Flooring (x41) | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 43 |
| L09-7138 | Electrical Trim-Out | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 37 |
| L09-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 27-Oct-14 | 29-Oct-14 | 37 |
| L10-7138 | Electrical Trim-Out | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 37 |
| L10-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 27-Oct-14 | 29-Oct-14 | 37 |
| L11-7138 | Electrical Trim-Out | 2 | 2 | 27-Oct-14 | 28-Oct-14 | 37 |
| L11-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 27-Oct-14 | 29-Oct-14 | 37 |

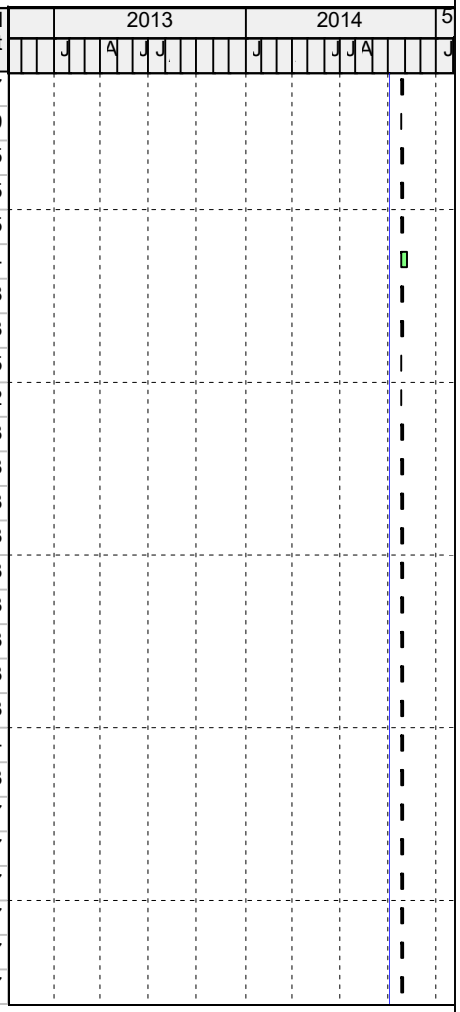



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8138 | Install Toilet Accessories | 4 | 4 | 27-Oct-14 | 30-Oct-14 | 24 |
| L02-8130 | L2 - Install ACT Grid | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 31 |
| L09-7144 | Fire Sprinkler Trim | 1 | 1 | 27-Oct-14 | 27-Oct-14 | 39 |
| L10-7144 | Fire Sprinkler Trim | 1 | 1 | 27-Oct-14 | 27-Oct-14 | 39 |
| L11-7144 | Fire Sprinkler Trim | 1 | 1 | 27-Oct-14 | 27-Oct-14 | 39 |
| SW-2120 | Zone 1 - Install irrigation | 10 | 10 | 27-Oct-14 | 07-Nov-14 | 54 |
| SW-2122 | Zone 1 - Install landscaping | 10 | 10 | 27-Oct-14 | 07-Nov-14 | 54 |
| SW-2212 | Zone 2 - FRP sidewalk | 3 | 3 | 27-Oct-14 | 29-Oct-14 | 36 |
| RF-4040 | L2.5 Horseshoe - Install sheet metal capping | 3 | 3 | 27-Oct-14 | 29-Oct-14 | 40 |
| MPP-1012 | Podium - Caulking, south | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 44 |
| CO-7164 | Genetator - Final electrical inspection | 1 | 1 | 27-Oct-14 | 27-Oct-14 | 27 |
| CO-7214 | Cx - Flush & Fill HVAC Hydronics Systems | 7 | 7 | 27-Oct-14 | 04-Nov-14 | 4 |
| CO-7126 | Fire pump test pre-planning complete (see checklist) | 0 | 0 |  | 27-Oct-14 | 30 |
| L04-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 28-Oct-14 | 29-Oct-14 | 41 |
| L05-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 28-Oct-14 | 29-Oct-14 | 41 |
| L06-8418 | Flooring at Elevator Lobby | 3 | 3 | 28-Oct-14 | 30-Oct-14 | 39 |
| L07-8418 | Flooring at Elevator Lobby | 3 | 3 | 28-Oct-14 | 30-Oct-14 | 39 |
| L08-8418 | Flooring at Elevator Lobby | 3 | 3 | 28-Oct-14 | 30-Oct-14 | 39 |
| L10-8129 | Install Shower Doors | 4 | 4 | 28-Oct-14 | 31-Oct-14 | 34 |
| L06-7134 | Install VCT Flooring | 3 | 3 | 28-Oct-14 | 30-Oct-14 | 39 |
| L07-7134 | Install VCT Flooring | 3 | 3 | 28-Oct-14 | 30-Oct-14 | 39 |
| L08-7134 | Install VCT Flooring | 3 | 3 | 28-Oct-14 | 30-Oct-14 | 39 |
| RF-4060 | Roof at Manlift - Install corrugated metal panels | 3 | 3 | 28-Oct-14 | 30-Oct-14 | 53 |
| MPT-1028 | Tower - Caulking, south | 6 | 6 | 28-Oct-14 | 04-Nov-14 | 52 |
| CO-7128 | Run fire pump test | 2 | 2 | 28-Oct-14 | 29-Oct-14 | 30 |
| L1BOH2-8140 | Acoustical Ceiling Tile | 4 | 4 | 29-Oct-14 | 03-Nov-14 | 21 |
| L03-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 29-Oct-14 | 30-Oct-14 | 40 |

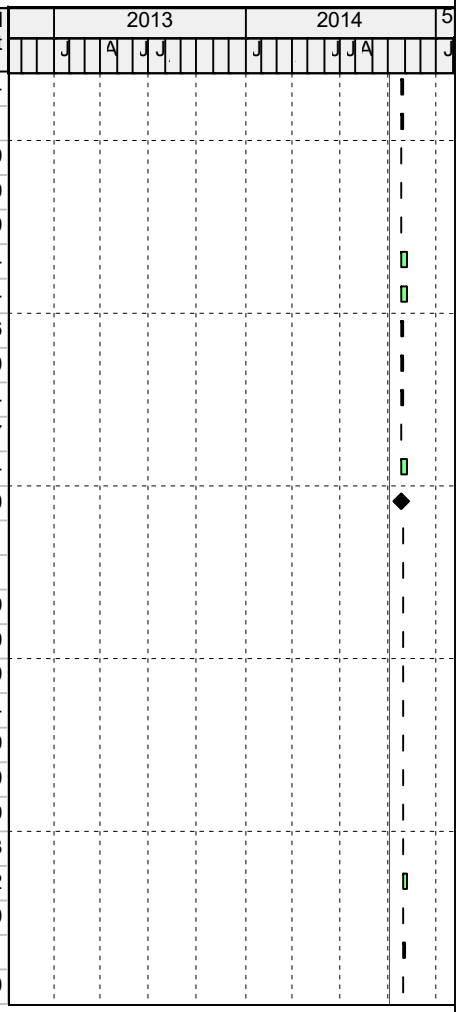



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 29-Oct-14 | 31-Oct-14 | 35 |
| L12-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 37 |
| L14-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 29-Oct-14 | 31-Oct-14 | 35 |
| L14-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 37 |
| L15-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 29-Oct-14 | 31-Oct-14 | 35 |
| L15-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 37 |
| L16-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 29-Oct-14 | 30-Oct-14 | 34 |
| L17-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 29-Oct-14 | 30-Oct-14 | 33 |
| L14-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 29-Oct-14 | 03-Nov-14 | 28 |
| L03-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 43 |
| L03-7136 | Install Doors and Hardware | 2 | 2 | 29-Oct-14 | 30-Oct-14 | 40 |
| L06-7044 | Install Vending Cabinets (x41) | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 43 |
| L07-7044 | Install Vending Cabinets (x41) | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 43 |
| L08-7044 | Install Vending Cabinets (x41) | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 43 |
| L09-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 43 |
| L10-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 43 |
| L11-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 43 |
| L12-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 43 |
| L14-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 43 |
| L15-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 43 |
| L16-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 44 |
| L17-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 43 |
| L04-7136 | Install Door and Hardware | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 41 |
| L05-7136 | Install Door and Hardware | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 41 |
| L12-7138 | Electrical Trim-Out | 2 | 2 | 29-Oct-14 | 30-Oct-14 | 35 |
| L12-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 29-Oct-14 | 31-Oct-14 | 35 |
| L14-7138 | Electrical Trim-Out | 2 | 2 | 29-Oct-14 | 30-Oct-14 | 35 |

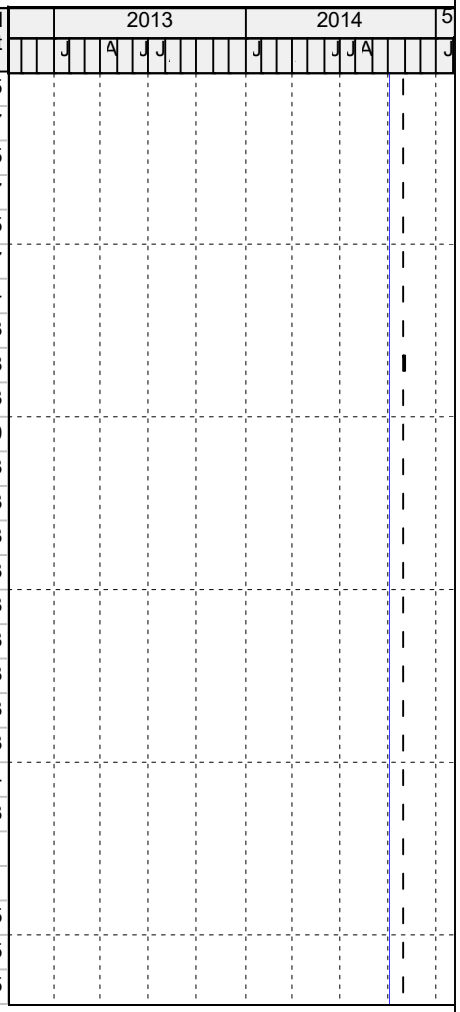



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 29-Oct-14 | 31-Oct-14 | 35 |
| L15-7138 | Electrical Trim-Out | 2 | 2 | 29-Oct-14 | 30-Oct-14 | 35 |
| L15-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 29-Oct-14 | 31-Oct-14 | 35 |
| L12-7144 | Fire Sprinkler Trim | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 37 |
| L14-7144 | Fire Sprinkler Trim | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 37 |
| L15-7144 | Fire Sprinkler Trim | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 37 |
| MPP-1016 | Podium - Caulking, east | 6 | 6 | 29-Oct-14 | 05-Nov-14 | 46 |
| L04-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 41 |
| L05-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 41 |
| L06-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 39 |
| L07-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 39 |
| L08-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 39 |
| L09-8418 | Flooring at Elevator Lobby | 3 | 3 | 30-Oct-14 | 03-Nov-14 | 37 |
| L10-8418 | Flooring at Elevator Lobby | 3 | 3 | 30-Oct-14 | 03-Nov-14 | 37 |
| L11-8418 | Flooring at Elevator Lobby | 3 | 3 | 30-Oct-14 | 03-Nov-14 | 37 |
| L1K-8340 | Install walk-in cooler/freezer (BY OTHERS) | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 12 |
| L11-8129 | Install Shower Doors | 4 | 4 | 30-Oct-14 | 04-Nov-14 | 29 |
| L16-8201 | Install ACT Grid @ Corridors | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 35 |
| L09-7134 | Install VCT Flooring | 3 | 3 | 30-Oct-14 | 03-Nov-14 | 37 |
| L10-7134 | Install VCT Flooring | 3 | 3 | 30-Oct-14 | 03-Nov-14 | 37 |
| L11-7134 | Install VCT Flooring | 3 | 3 | 30-Oct-14 | 03-Nov-14 | 37 |
| L10-8138 | Install Toilet Accessories | 4 | 4 | 30-Oct-14 | 04-Nov-14 | 23 |
| L17-8136 | Install Counter Subtops | 3 | 3 | 30-Oct-14 | 03-Nov-14 | 29 |
| L04-7146 | Final Coat Finish Paint | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 41 |
| L05-7146 | Final Coat Finish Paint | 2 | 2 | 30-Oct-14 | 31-Oct-14 | 41 |
| SW-2216 | Zone 2 - Install irrigation | 10 | 10 | 30-Oct-14 | 12-Nov-14 | 51 |
| SW-2218 | Zone 2 - Install landscaping | 10 | 10 | 30-Oct-14 | 12-Nov-14 | 51 |

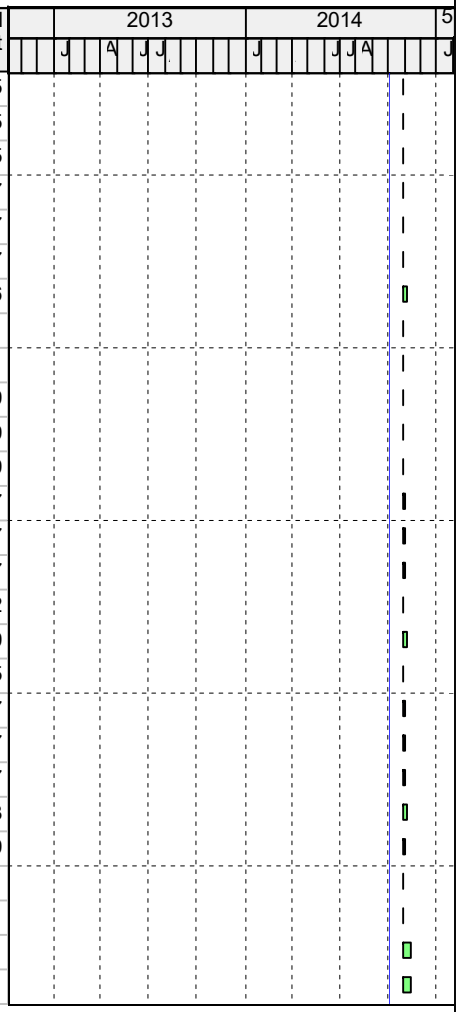



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| RF-4064 | Pool Green Roof - Install sheet metal capping | 3 | 3 | 30-Oct-14 | 03-Nov-14 | 40 |
| L03-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 31-Oct-14 | 03-Nov-14 | 40 |
| L16-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 34 |
| L16-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 31-Oct-14 | 31-Oct-14 | 36 |
| L17-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 33 |
| L17-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 31-Oct-14 | 31-Oct-14 | 35 |
| L1K-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 31-Oct-14 | 03-Nov-14 | 12 |
| L15-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 31-Oct-14 | 05-Nov-14 | 28 |
| L06-7136 | Install Door and Hardware | 1 | 1 | 31-Oct-14 | 31-Oct-14 | 39 |
| L07-7136 | Install Door and Hardware | 1 | 1 | 31-Oct-14 | 31-Oct-14 | 39 |
| L08-7136 | Install Door and Hardware | 1 | 1 | 31-Oct-14 | 31-Oct-14 | 39 |
| L16-7138 | Electrical Trim-Out | 2 | 2 | 31-Oct-14 | 03-Nov-14 | 34 |
| L16-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 34 |
| L17-7138 | Electrical Trim-Out | 2 | 2 | 31-Oct-14 | 03-Nov-14 | 33 |
| L17-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 33 |
| L06-8206a | Install Base @ Corridors | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 39 |
| L03-7146 | Final Coat Finish Paint | 2 | 2 | 31-Oct-14 | 03-Nov-14 | 40 |
| L16-7144 | Fire Sprinkler Trim | 1 | 1 | 31-Oct-14 | 31-Oct-14 | 36 |
| L17-7144 | Fire Sprinkler Trim | 1 | 1 | 31-Oct-14 | 31-Oct-14 | 35 |
| RF-4062 | Roof at Manlift - Install sheet metal capping | 2 | 2 | 31-Oct-14 | 03-Nov-14 | 53 |
| L06-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 39 |
| L07-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 39 |
| L08-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 39 |
| L09-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 37 |
| L10-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 37 |
| L11-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 37 |
| L12-8418 | Flooring at Elevator Lobby | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 35 |

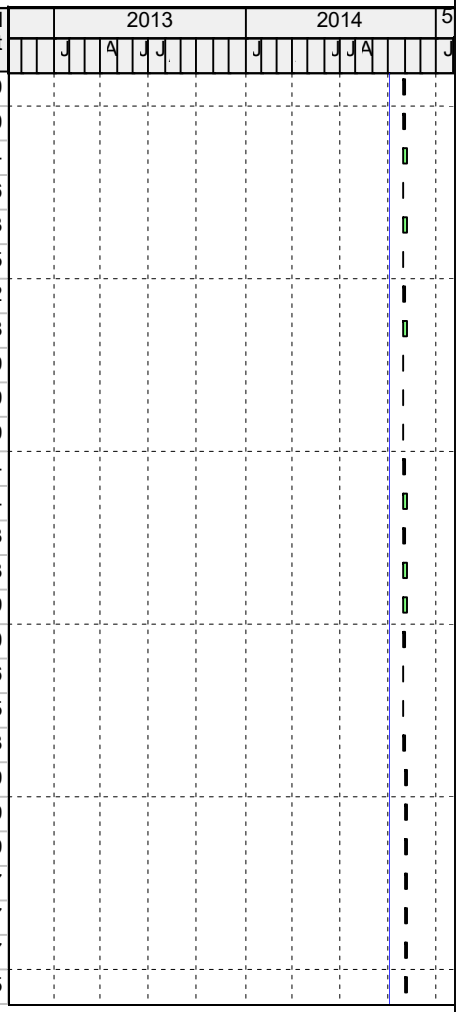



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8418 | Flooring at Elevator Lobby | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 35 |
| L15-8418 | Flooring at Elevator Lobby | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 35 |
| MPT-1012 | Tower - Install N/S Wing, S. End Concrete (Elev 33,34 | 10 | 10 | 03-Nov-14 | 14-Nov-14 | 44 |
| L12-8129 | Install Shower Doors | 4 | 4 | 03-Nov-14 | 06-Nov-14 | 29 |
| L12-7134 | Install VCT Flooring | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 35 |
| L14-7134 | Install VCT Flooring | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 35 |
| L15-7134 | Install VCT Flooring | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 35 |
| L06-7146 | Final Coat Finish Paint | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 39 |
| L07-7146 | Final Coat Finish Paint | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 39 |
| L08-7146 | Final Coat Finish Paint | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 39 |
| SW-2308 | Zone 3 - Install lighting conduit | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 28 |
| SW-2310 | Zone 3 - Install irrigation sleeves | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 28 |
| MPP-1014 | Podium - Caulking, west | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 44 |
| CO-7130 | Fire Alarm - Point-To-Point Wiring | 18 | 18 | 03-Nov-14* | 26-Nov-14 | 4 |
| L1BOH2-8200 | First Coat Finish Paint | 5 | 5 | 04-Nov-14 | 10-Nov-14 | 21 |
| L09-7136 | Install Door and Hardware | 1 | 1 | 04-Nov-14 | 04-Nov-14 | 37 |
| L10-7136 | Install Door and Hardware | 1 | 1 | 04-Nov-14 | 04-Nov-14 | 37 |
| L11-7136 | Install Door and Hardware | 1 | 1 | 04-Nov-14 | 04-Nov-14 | 37 |
| L11-8138 | Install Toilet Accessories | 4 | 4 | 04-Nov-14 | 07-Nov-14 | 22 |
| L07-8206a | Install Base @ Corridors | 3 | 3 | 04-Nov-14 | 06-Nov-14 | 37 |
| SW-2312 | Zone 3 - Fine grade for sidewalk (excl. manlift area) | 3 | 3 | 04-Nov-14 | 06-Nov-14 | 28 |
| L09-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 37 |
| L10-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 37 |
| L11-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 37 |
| L12-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 35 |
| L15-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 35 |
| L16-8418 | Flooring at Elevator Lobby | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 34 |

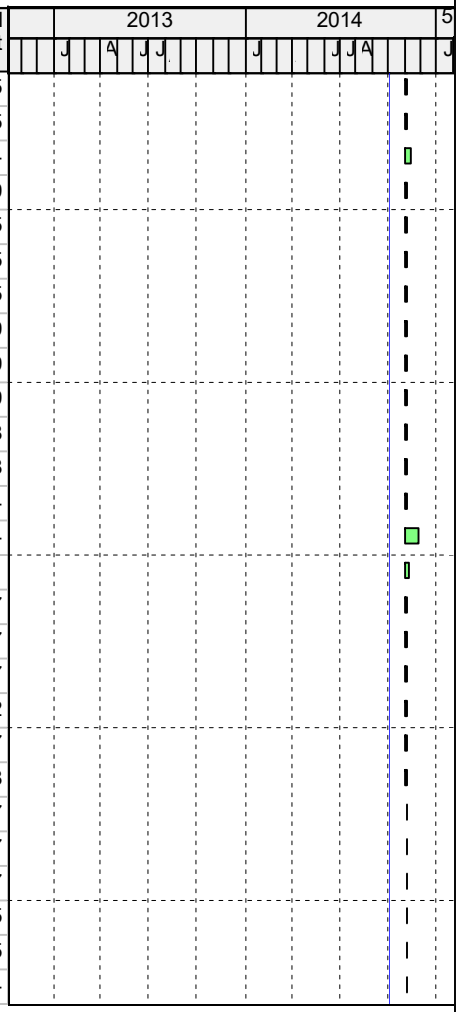



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8418 | Flooring at Elevator Lobby | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 33 |
| L14-8129 | Install Shower Doors | 4 | 4 | 05-Nov-14 | 10-Nov-14 | 29 |
| L16-7134 | Install VCT Flooring | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 34 |
| L17-7134 | Install VCT Flooring | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 33 |
| L09-7146 | Final Coat Finish Paint | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 37 |
| L10-7146 | Final Coat Finish Paint | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 37 |
| L11-7146 | Final Coat Finish Paint | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 37 |
| CO-7216 | Cx - Glycol Add/Circulate | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 4 |
| L14-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 06-Nov-14 | 07-Nov-14 | 35 |
| L16-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 06-Nov-14 | 11-Nov-14 | 26 |
| L17-8201 | Install ACT Grid @ Corridors | 2 | 2 | 06-Nov-14 | 07-Nov-14 | 32 |
| L12-7136 | Install Door and Hardware | 1 | 1 | 06-Nov-14 | 06-Nov-14 | 35 |
| L14-7136 | Install Door and Hardware | 1 | 1 | 06-Nov-14 | 06-Nov-14 | 35 |
| L15-7136 | Install Door and Hardware | 1 | 1 | 06-Nov-14 | 06-Nov-14 | 35 |
| L08-8206a | Install Base @ Corridors | 3 | 3 | 06-Nov-14 | 10-Nov-14 | 38 |
| SW-2314 | Zone 3 - FRP sidewalk (excl. manlift area) | 3 | 3 | 06-Nov-14 | 10-Nov-14 | 28 |
| L12-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 35 |
| L14-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 35 |
| L15-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 35 |
| L16-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 34 |
| L17-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 33 |
| L15-8129 | Install Shower Doors | 4 | 4 | 07-Nov-14 | 12-Nov-14 | 29 |
| L12-8138 | Install Toilet Accessories | 4 | 4 | 07-Nov-14 | 12-Nov-14 | 21 |
| L09-8206a | Install Base @ Corridors | 3 | 3 | 07-Nov-14 | 11-Nov-14 | 38 |
| L12-7146 | Final Coat Finish Paint | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 35 |
| L14-7146 | Final Coat Finish Paint | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 35 |
| L15-7146 | Final Coat Finish Paint | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 35 |

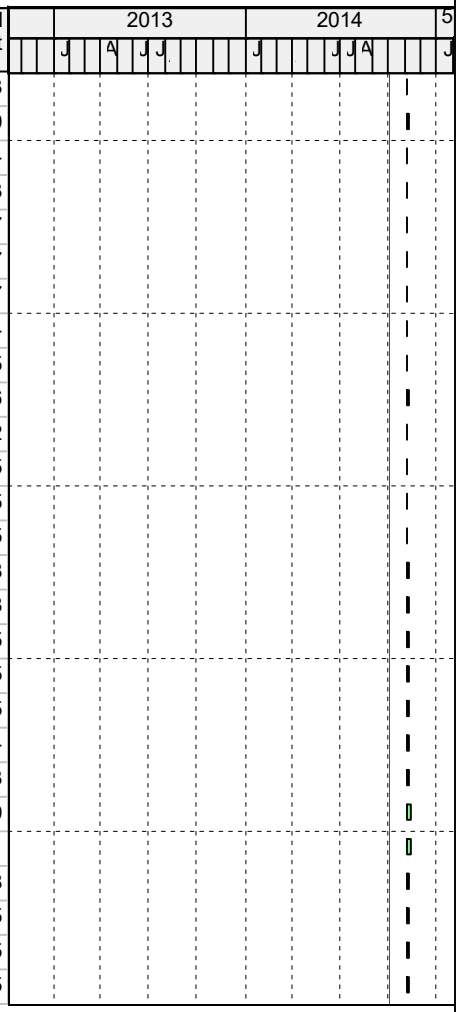



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7100T | Cx - Equipment Start-Up & Testing, Tower | 10 | 10 | 10-Nov-14 | 21-Nov-14 | 7 |
| L16-7136 | Install Door and Hardware | 1 | 1 | 10-Nov-14 | 10-Nov-14 | 34 |
| L17-7136 | Install Door and Hardware | 1 | 1 | 10-Nov-14 | 10-Nov-14 | 33 |
| L1B-8102a | GWB Hang/Tape (Ceilings) | 12 | 12 | 10-Nov-14 | 25-Nov-14 | 1 |
| L02-8138 | L2 - Install ceiling tile | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 31 |
| MPP-1018 | Podium - Caulking, north | 5 | 5 | 10-Nov-14 | 14-Nov-14 | 44 |
| CO-7400 | Cx - 3rd Party Cx of Mechanical, Plumbing, Electrical | 40 | 40 | 10-Nov-14 | 09-Jan-15 | 4 |
| CO-7218 | Cx - Start-Up & Test Hydronics System, Tower | 10 | 10 | 10-Nov-14 | 21-Nov-14 | 44 |
| CO-7220 | Cx - Start-Up & Test Hydronics System, Podium | 18 | 18 | 10-Nov-14 | 05-Dec-14 | 4 |
| L1BOH2-8124 | Flooring | 4 | 4 | 11-Nov-14 | 14-Nov-14 | 21 |
| L16-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 34 |
| L17-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 33 |
| L16-8129 | Install Shower Doors | 4 | 4 | 11-Nov-14 | 14-Nov-14 | 29 |
| L14-8138 | Install Toilet Accessories | 4 | 4 | 11-Nov-14 | 14-Nov-14 | 21 |
| L16-7146 | Final Coat Finish Paint | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 34 |
| L17-7146 | Final Coat Finish Paint | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 33 |
| RF-4066 | Pool Green Roof - Install decorative metal railing | 3 | 3 | 11-Nov-14 | 13-Nov-14 | 39 |
| L17-8129 | Install Shower Doors | 4 | 4 | 13-Nov-14 | 18-Nov-14 | 29 |
| L17-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 13-Nov-14 | 18-Nov-14 | 24 |
| L10-8206a | Install Base @ Corridors | 3 | 3 | 13-Nov-14 | 15-Nov-14 | 42 |
| L03-8638 | Pool - Install pool deck and ADA lift | 3 | 3 | 14-Nov-14 | 18-Nov-14 | 9 |
| L1BOH2-8124a | Install Base | 3 | 3 | 14-Nov-14 | 18-Nov-14 | 21 |
| RF-4068 | Pool Green Roof - Install American Hydrotech assem | 3 | 3 | 14-Nov-14 | 18-Nov-14 | 39 |
| I-1602 | Enclosure at manlift - Install air barrier | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 19 |
| CO-7102T | Cx - DDC Point-To-Point Checks, Tower | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 39 |
| L15-8138 | Install Toilet Accessories | 4 | 4 | 17-Nov-14 | 20-Nov-14 | 19 |
| L1L-8102a | GWB Hang/Tape (Ceilings) | 11 | 11 | 17-Nov-14 | 03-Dec-14 | 0 |

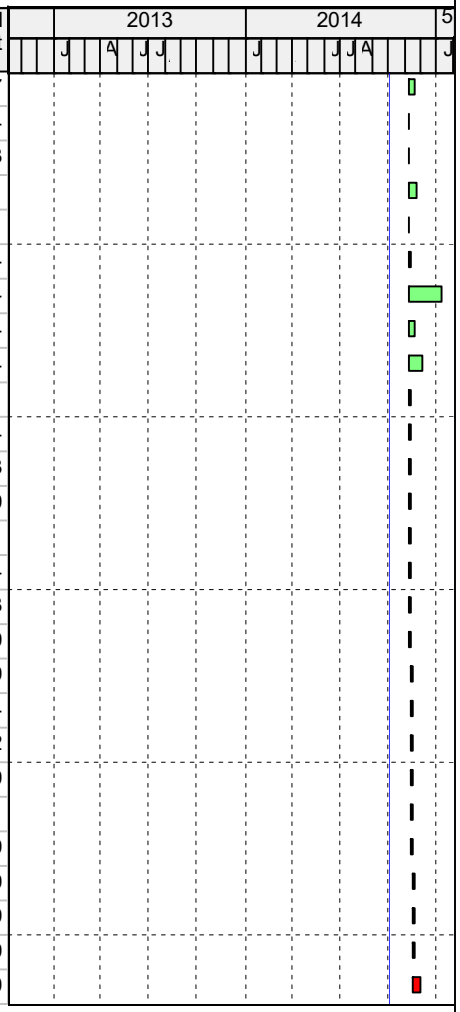



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-8124a | Install Base | 3 | 3 | 17-Nov-14 | 19-Nov-14 | 19 |
| SW-2316 | Zone 3 - Demolish manlift shack and base | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 31 |
| L1BOH2-8116 | Finish Carpentry / Millwork | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 21 |
| L1BOH2-8126 | Doors & Hardware | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 25 |
| LL1-Z2-8108 | Install Junior Balllroom ceiling feature (allowance) | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 19 |
| L03-8606 | L3 Pool - HVAC R/I | 3 | 3 | 18-Nov-14 | 20-Nov-14 | 9 |
| L1K-8124a | Install Flooring (Epoxy) | 8 | 8 | 18-Nov-14 | 26-Nov-14 | 14 |
| L11-8206a | Install Base @ Corridors | 3 | 3 | 18-Nov-14 | 20-Nov-14 | 38 |
| L03-8640 | Pool - Prep and install plaster | 2 | 2 | 19-Nov-14 | 20-Nov-14 | 9 |
| LL1-8124a | Install Base | 4 | 4 | 19-Nov-14 | 24-Nov-14 | 22 |
| RF-4070 | TR - Terrace Roof - Install American Hydrotech assem | 3 | 3 | 19-Nov-14 | 21-Nov-14 | 39 |
| MPT-1040 | Tower - Install N/S Wing, S, End (Elev 30) | 6 | 6 | 19-Nov-14 | 26-Nov-14 | 19 |
| L16-8138 | Install Toilet Accessories | 4 | 4 | 20-Nov-14 | 25-Nov-14 | 18 |
| L1BOH2-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 21-Nov-14 | 24-Nov-14 | 21 |
| L1BOH2-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 21-Nov-14 | 24-Nov-14 | 21 |
| L1BOH2-8204 | Mech Trim / Finish (HVAC & Plumbing) | 2 | 2 | 21-Nov-14 | 24-Nov-14 | 21 |
| LL1-Z3-8340 | Install walk-in cooler/freezer (BY OTHERS) | 5 | 5 | 21-Nov-14* | 01-Dec-14 | 25 |
| L03-8612 | L3 Pool - GWB hang/tape/finish | 5 | 5 | 21-Nov-14 | 01-Dec-14 | 9 |
| L03-8642 | Pool - Fill pool | 2 | 2 | 21-Nov-14 | 24-Nov-14 | 35 |
| L12-8206a | Install Base @ Corridors | 3 | 3 | 21-Nov-14 | 24-Nov-14 | 35 |
| LL1-Z2-8118a | Install decorative light fixtures | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 25 |
| L14-8206a | Install Base @ Corridors | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 33 |
| SW-2318 | Zone 3 - Fine grade for sidewalk at manlift | 1 | 1 | 24-Nov-14 | 24-Nov-14 | 31 |
| MPT-1042 | Enclosure at manlift - Insulation | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 19 |
| L1BOH2-8201 | Final Coat Finish Paint | 5 | 5 | 25-Nov-14 | 03-Dec-14 | 25 |
| L03-8644 | Pool - Start-up and adjust pool equipment | 2 | 2 | 25-Nov-14 | 26-Nov-14 | 35 |
| L17-8138 | Install Toilet Accessories | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 17 |

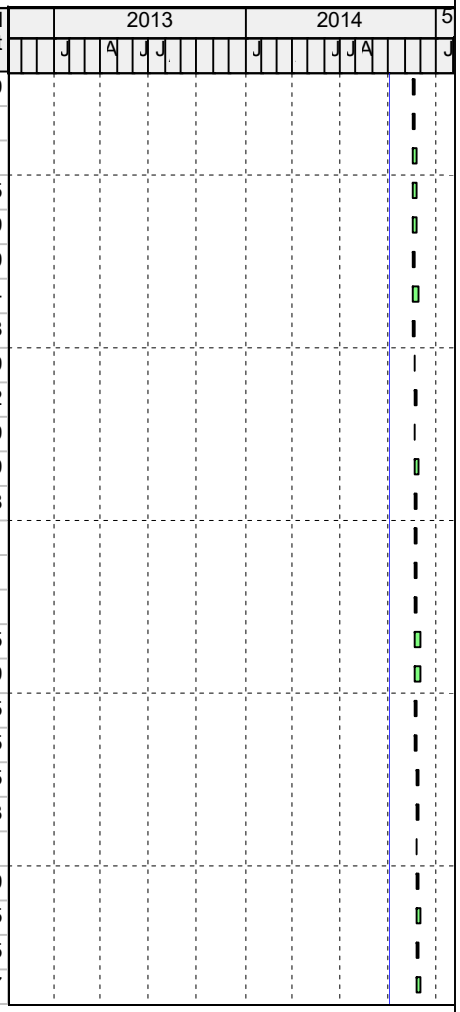



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2320 | Zone 3 - FRP sidewalk at manlift | 2 | 2 | 25-Nov-14 | 26-Nov-14 | 31 |
| L03-8206a | Install Base @ Corridors | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 21 |
| CO-7110T | Fire Sprinkler Pre-Testing (Tower) | 15 | 15 | 01-Dec-14 | 19-Dec-14 | 4 |
| CO-7116T | Fire Alarm Pre-Testing (Tower) | 15 | 15 | 01-Dec-14 | 19-Dec-14 | 4 |
| CO-7104T | Smoke Control Pre-Testing (Tower) | 15 | 15 | 01-Dec-14 | 19-Dec-14 | 4 |
| L03-8646 | Pool - Health inspections | 1 | 1 | 01-Dec-14 | 01-Dec-14 | 35 |
| L1K-8124b | Install Base | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 18 |
| SW-2322 | Zone 3 - Install irrigation | 10 | 10 | 01-Dec-14 | 12-Dec-14 | 31 |
| SW-2324 | Zone 3 - Install landscaping | 10 | 10 | 01-Dec-14 | 12-Dec-14 | 31 |
| MPT-1044 | Tower - Install sign backing south | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 19 |
| LL1-Z3-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 02-Dec-14* | 03-Dec-14 | 25 |
| L03-8614 | L3 Pool - Paint/wall finishes | 3 | 3 | 02-Dec-14 | 04-Dec-14 | 11 |
| L03-8618 | L3 Pool - Ceramic tile | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 9 |
| L15-8206a | Install Base @ Corridors | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 28 |
| CO-7222 | Cx - Kitchen Equipment Start-Up & Testing | 15 | 15 | 03-Dec-14 | 23-Dec-14 | 24 |
| CO-7224 | Cx - Food Prep Equipment Start-Up & Testing | 15 | 15 | 03-Dec-14 | 23-Dec-14 | 24 |
| CO-7226 | Cx - Laundry Equipment Start-Up & Testing | 15 | 15 | 03-Dec-14 | 23-Dec-14 | 24 |
| CO-7228 | Cx - Pool Equipment Start-Up & Testing | 15 | 15 | 03-Dec-14 | 23-Dec-14 | 24 |
| L1BOH2-8134 | Clean | 4 | 4 | 04-Dec-14 | 09-Dec-14 | 25 |
| L1BOH2-8132 | Punch | 4 | 4 | 04-Dec-14 | 09-Dec-14 | 25 |
| I-1610 | Enclosure at manlift - Framing and windows | 4 | 4 | 04-Dec-14 | 09-Dec-14 | 19 |
| L16-8206a | Install Base @ Corridors | 3 | 3 | 05-Dec-14 | 08-Dec-14 | 23 |
| CO-7230 | Cx - TAB: Air Moving Systems, Tower | 10 | 10 | 08-Dec-14 | 19-Dec-14 | 26 |
| CO-7232 | Cx - TAB: Plumbing/HVAC Water Systems, Tower | 10 | 10 | 08-Dec-14 | 19-Dec-14 | 26 |
| CO-7234 | Cx - TAB: Air Moving Systems, Podium | 17 | 17 | 08-Dec-14 | 02-Jan-15 | 19 |
| CO-7236 | Cx - TAB: Plumbing/HVAC Water Systems, Podium | 17 | 17 | 08-Dec-14 | 02-Jan-15 | 19 |
| CO-7238 | Cx - Internal Equipment Verifications (HP) | 17 | 17 | 08-Dec-14 | 02-Jan-15 | 4 |

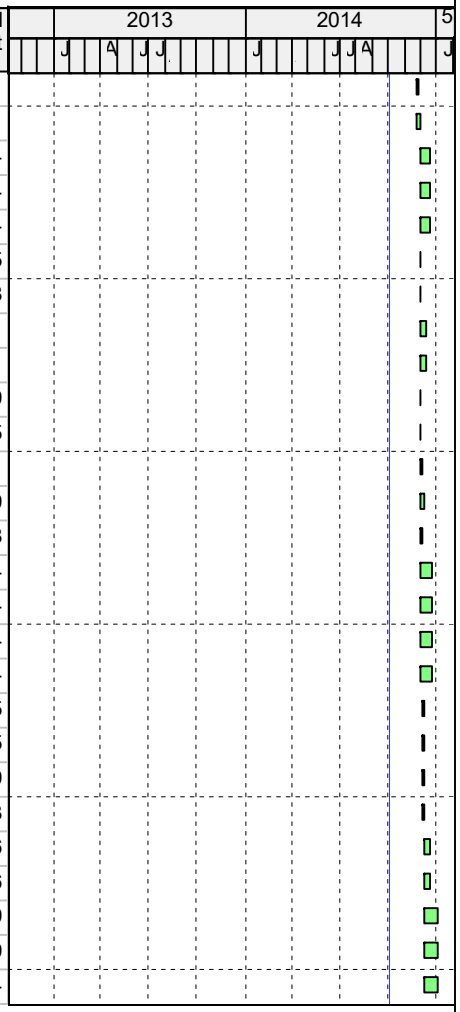



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8620 | L3 Pool - Plumbing Fixtures & Trim / Finish | 5 | 5 | 09-Dec-14 | 15-Dec-14 | 9 |
| L03-8622 | L3 Pool - HVAC trim / Finish | 5 | 5 | 09-Dec-14 | 15-Dec-14 | 9 |
| L03-8624 | L3 Pool - Fire Sprinkler Trim / Finish | 5 | 5 | 09-Dec-14 | 15-Dec-14 | 9 |
| L03-8626 | L3 Pool - Elec Trim/ Finish | 5 | 5 | 09-Dec-14 | 15-Dec-14 | 9 |
| L03-8628 | L3 Pool - Elec Specialties Trim / Finish | 5 | 5 | 09-Dec-14 | 15-Dec-14 | 9 |
| L1BOH2-8210 | Owner Walk / Create Punchlist | 1 | 1 | 10-Dec-14 | 10-Dec-14 | 25 |
| I-1604 | Enclosure at manlift - GWB | 6 | 6 | 10-Dec-14 | 17-Dec-14 | 23 |
| I-1608 | Enclosure at manlift - Metal panels (Elev 32) | 5 | 5 | 10-Dec-14 | 16-Dec-14 | 19 |
| L17-8206a | Install Base @ Corridors | 3 | 3 | 10-Dec-14 | 12-Dec-14 | 22 |
| L1BOH2-8212 | Resolve Final Punchlist | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 25 |
| I-1606 | Enclosure at manlift - Paint & finishes | 4 | 4 | 12-Dec-14 | 17-Dec-14 | 23 |
| L1BOH2-81214 | L1, Zone 3 Complete | 0 | 0 | | 15-Dec-14 | 25 |
| CM-1024 | Tower - "Clean/Punch" Complete - All Floors | 0 | 0 | | 15-Dec-14 | 30 |
| L03-8630 | L3 Pool - Doors & Hardware | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 9 |
| I-1612 | Enclosure at manlift - Caulking (Elev 32) | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 19 |
| I-3102 | Ballroom ceilings - additional work per ASIs 18, 25 | 4 | 4 | 18-Dec-14 | 23-Dec-14 | 4 |
| L1B-8120 | Install operable partitions | 3 | 3 | 18-Dec-14 | 22-Dec-14 | 5 |
| L1B-8128 | Install Base | 2 | 2 | 18-Dec-14 | 19-Dec-14 | 6 |
| L1K-8128 | Install Kitchen equipment (BY OTHERS) | 10 | 10 | 19-Dec-14 | 06-Jan-15 | 12 |
| L03-8632 | L3 Pool - Install Bathroom Accessories | 3 | 3 | 23-Dec-14 | 29-Dec-14 | 9 |
| L1L-8124a | Install Base | 3 | 3 | 24-Dec-14 | 30-Dec-14 | 2 |
| I-1202 | Concierge Lounge - Additional flooring work | 1 | 1 | 29-Dec-14 | 29-Dec-14 | 0 |
| I-1204 | Concierge Lounge - Additional millwork | 4 | 4 | 29-Dec-14 | 02-Jan-15 | 0 |
| L1L-8120 | Install plumbing at bar | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 2 |
| L1L-8122 | Install electrical at bar | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 2 |
| CO-7112T | City of Bellevue/3rd Party Fire Sprinkler Inspection / A | 5 | 5 | 12-Jan-15 | 16-Jan-15 | 4 |
| CO-7118T | City of Bellevue/3rd Party Fire Alarm Inspection / Appl | 5 | 5 | 12-Jan-15 | 16-Jan-15 | 4 |

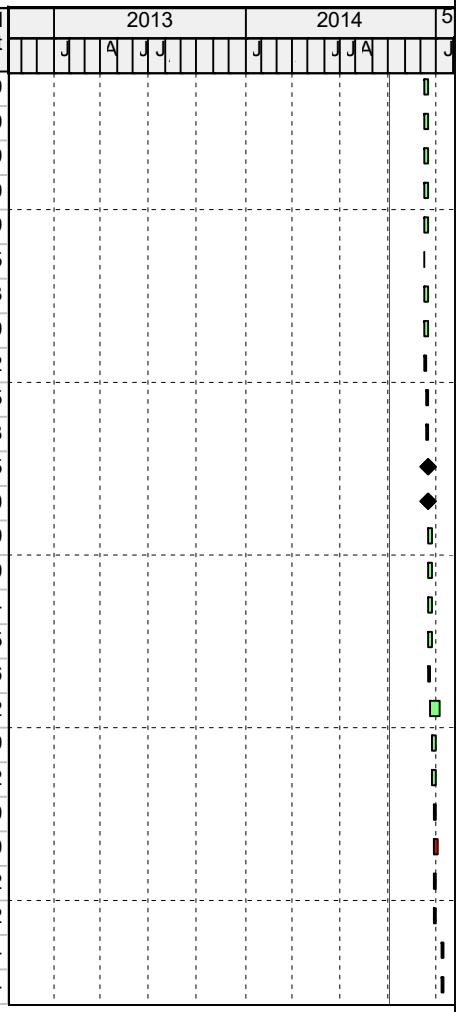



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7106T | City of Bellevue/3rd Party Smoke Control Testing (Tow | 5 | 5 | 12-Jan-15 | 16-Jan-15 | 4 |
| CO-7402 | Cx - Final 3rd Party Commissioning | 10 | 10 | 12-Jan-15 | 23-Jan-15 | 4 |
| CM-1022 | Podium - "Clean/Punch" Complete - All Floors, All Zon | 0 | 0 | | 15-Jan-15 | 10 |
| CO-7124 | Complete Final Building Inspections | 5 | 5 | 23-Jan-15 | 29-Jan-15 | 0 |
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13 A | | |
| CM-1002 | CM - Contract Time (578 Cal Days) | 576 | 0 | 06-Mar-13 A | 05-Oct-14 A | |
| CM-1014 | CM - Start of Construction | 0 | 0 | 05-Apr-13 A | | |
| CM-1006 | Construction Documents Issued by Client - (Due on 7 | 0 | 0 | 06-Oct-14 | | 116 |
| CM-1008 | Finalization of Allowances - (Due on 9-2-13) | 0 | 0 | 06-Oct-14 | | 116 |
| CO-7004 | CO - Prep / Submit O&M Manuals | 40 | 40 | 25-Oct-14 | 03-Dec-14 | 57 |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 14-Nov-14 | | 35 |
| CM-1016 | CM - Owner FF+E "Build-Out" | 42 | 42 | 14-Nov-14 | 25-Dec-14 | 35 |
| CM-1018 | CM - Hotel Operations Training | 21 | 21 | 29-Nov-14* | 19-Dec-14 | 41 |
| CO-7006 | CO - Certificate of Occupancy/Substantial Completior | 0 | 0 | | 29-Jan-15 | 0 |
| CO-7122 | CO - Certificate of Occupancy | 0 | 0 | | 29-Jan-15 | 0 |
| **Misc Milestones** | | | | | | |
| CM-1020 | MM - Site Mobilization | 10 | 0 | 06-Mar-13 A | 04-Apr-13 A | |
| MM-1008 | MM - Top Out - Tower / Structure | 0 | 0 | | 16-Apr-14 A | |
| MM-1004 | MM - Start Drywall In Tower | 0 | 0 | 27-Jun-14 A | | |
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 06-Sep-14 A | |
| MM-1010 | Energize Permanent Power | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| **Tower Crane** | | | | | | |

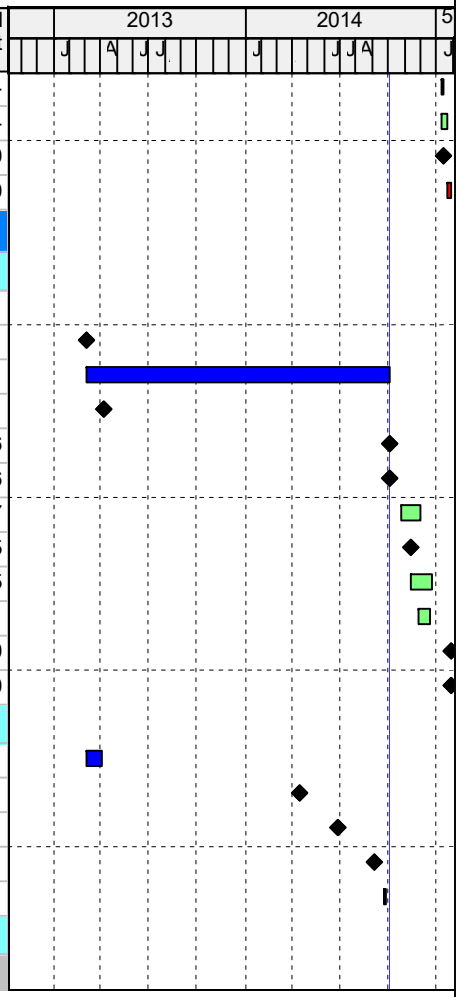



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 0 | 04-Jun-13 A | 14-Jun-13 A | |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 0 | 20-Jun-13 A | 24-Jun-13 A | |
| TC-5902 | Tower Crane - Erectiion | 2 | 0 | 21-Jun-13 A | 24-Jun-13 A | |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 24-Jun-13 A | | |
| TC-5906 | Tower Crane - Operatational Period | 391 | 0 | 24-Jun-13 A | 16-Jun-14 A | |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 0 | 16-Jun-14 A | 17-Jun-14 A | |
| **Man & Material Lifts** | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 0 | 14-Jan-14 A | 20-Jan-14 A | |
| ML-5952 | Man/Material Lifts - Erect/Build Loading Dock | 5 | 0 | 21-Jan-14 A | 27-Jan-14 A | |
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 10-Feb-14 A | | |
| ML-5954 | Man/Material Lifts - Load Test / Certify | 1 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| ML-5958 | Man/Material Lifts - Operatational Period | 196 | 40 | 10-Feb-14 A | 14-Nov-14 | 29 |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 2 | 2 | 15-Nov-14 | 16-Nov-14 | 29 |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |
| **Mass Excavation / Shoring** | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 0 | 05-Apr-13 A | 12-Apr-13 A | |
| SW-2002 | Demolition And Utility Relocation | 8 | 0 | 15-Apr-13 A | 19-Apr-13 A | |
| SW-2010 | Grade Subgrade for Elect/Plumbing | 3 | 0 | 07-Jan-14 A | 09-Jan-14 A | |
| **Site Finishes** | | | | | | |
| SW-2006 | Install Perm Power Electrical Service / Dry Utilities (Off | 15 | 0 | 20-May-14 A | 05-Jun-14 A | |
| SW-2004 | Offsite Water & Water Connection | 9 | 0 | 22-Sep-14 A | 01-Oct-14 A | |
| SW-2008 | Zone 4 - Site finishes (summarized) | 20 | 20 | 10-Nov-14 | 18-Dec-14 | 22 |
| **Structure** | | | | | | |
| **Foundation / Substructure - (Levels LL4 / LL3)** | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |

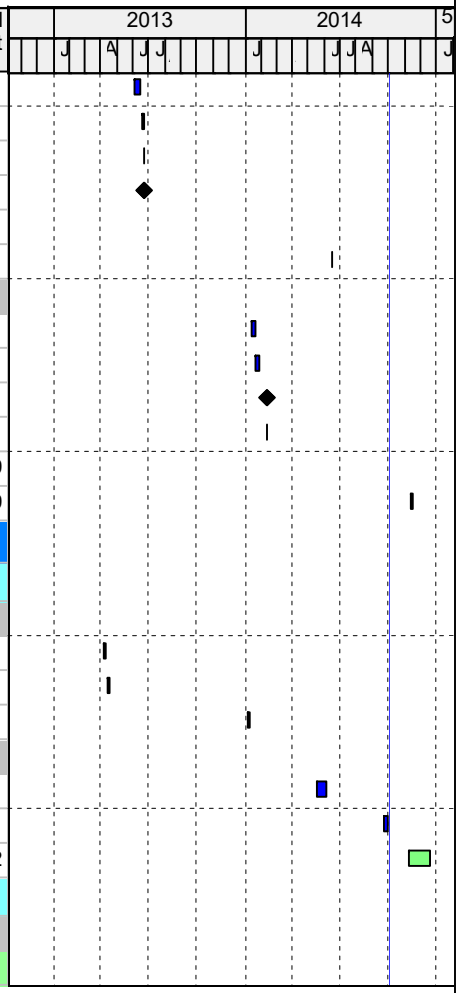



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 0 | 12-Jun-13 A | 27-Jun-13 A | |
| LL4-1601 | LL4 - Excavate Footings | 14 | 0 | 17-Jun-13 A | 30-Jul-13 A | |
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 0 | 18-Jun-13 A | 24-Jun-13 A | |
| LL4-1606 | LL4 - Undrgmd Plumbing | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-1608 | LL4 - Undrgmd Elec | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 0 | 19-Jun-13 A | 25-Jun-13 A | |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 0 | 26-Jun-13 A | 02-Aug-13 A | |
| LL4-2033 | LL4 - Shotcrete Walls | 27 | 0 | 26-Jun-13 A | 05-Aug-13 A | |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 0 | 03-Jul-13 A | 21-Aug-13 A | |
| LL4-1614 | LL4 - FRP SOG | 5 | 0 | 10-Jul-13 A | 07-Aug-13 A | |
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 0 | 12-Jul-13 A | 26-Jul-13 A | |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 0 | 13-Jul-13 A | 06-Aug-13 A | |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 0 | 22-Jul-13 A | 24-Jul-13 A | |
| LL4-1618 | LL4 - FRP Ramp SOG | 5 | 0 | 01-Aug-13 A | 07-Aug-13 A | |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2004 | LL2 - Shore / Form Deck | 8 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2006 | LL3 - M & E Inserts | 4 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2008 | LL3 - ReSteel / PT Cables | 6 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2010 | LL3 - Install Embeds | 2 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2001 | LL3 - Waterproof Walls | 3 | 0 | 05-Aug-13 A | 05-Aug-13 A | |
| LL3-2012 | LL3 - Pour / Finish Deck | 2 | 0 | 16-Aug-13 A | 16-Aug-13 A | |
| LL3-2014 | LL3 - Stress Tendons | 1 | 0 | 19-Aug-13 A | 19-Aug-13 A | |
| LL3-2000 | LL3 - FRP Core Walls | 8 | 0 | 19-Aug-13 A | 28-Aug-13 A | |
| LL3-2033 | LL3 - Shotcrete Walls | 5 | 0 | 23-Aug-13 A | 26-Aug-13 A | |
| LL3-2016 | LL3 - Strip / ReShore Deck | 3 | 0 | 01-Sep-13 A | 13-Sep-13 A | |
| LL3-2018 | LL3 - Remove ReShores | 4 | 0 | 04-Nov-13 A | 07-Nov-13 A | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |

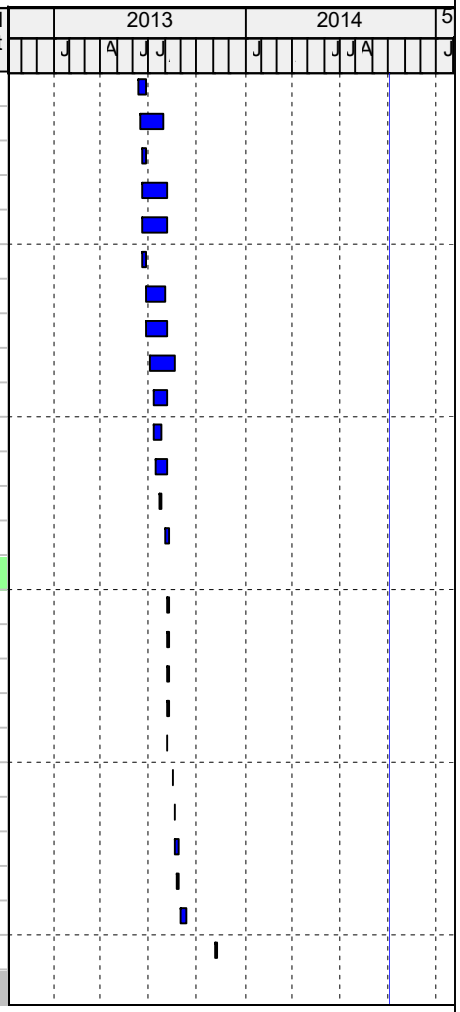



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Grids 1 to 4 - (SOG @ Loading Dock)** | | | | | | |
| LL2-2056 | LL2 - Grease Intercepter | 5 | 0 | 15-Aug-13 A | 21-Aug-13 A | |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 0 | 27-Aug-13 A | 04-Sep-13 A | |
| LL2-2027 | LL2 - Waterproof Walls | 2 | 0 | 27-Aug-13 A | 28-Aug-13 A | |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 0 | 30-Aug-13 A | 05-Sep-13 A | |
| LL2-2021 | LL2 - FRP Elec Vault | 14 | 0 | 30-Aug-13 A | 04-Sep-13 A | |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 0 | 04-Sep-13 A | 11-Sep-13 A | |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 0 | 11-Sep-13 A | 13-Sep-13 A | |
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls/Roof | 11 | 0 | 19-Sep-13 A | 03-Oct-13 A | |
| LL2-2020 | LL2 - Undrgmd Plumbing | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2022 | LL2 - Undrgmd Elec | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2031 | LL2 - FRP Generator SOG | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2015 | LL2 to LL1 FRP Columns / Misc Walls | 6 | 0 | 01-Oct-13 A | 01-Oct-13 A | |
| LL2-2029 | LL2 - F/R/P Pour #2 | 8 | 0 | 15-Jan-14 A | 24-Jan-14 A | |
| LL2-2011 | LL2 - F/R/P Pour #3 | 16 | 0 | 24-Jan-14 A | 18-Feb-14 A | |
| LL2-2019 | LL2 - F/R/P Pour #6 | 4 | 0 | 19-Feb-14 A | 17-Mar-14 A | |
| LL2-2044 | LL2 - Set Generator | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |
| LL2-2004 | LL2 - Shore / Form Deck | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2035 | LL2 to LL1 - Shotcrete Walls | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2006 | LL2 - M & E Inserts | 4 | 0 | 14-Aug-13 A | 19-Aug-13 A | |
| LL2-2008 | LL2 - ReSteel / PT Cables | 6 | 0 | 14-Aug-13 A | 21-Aug-13 A | |
| LL2-2010 | LL2 - Install Embeds | 3 | 0 | 14-Aug-13 A | 16-Aug-13 A | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 0 | 27-Aug-13 A | 06-Sep-13 A | |
| LL2-2012 | LL2 - Place / Finish Deck | 3 | 0 | 29-Aug-13 A | 29-Aug-13 A | |

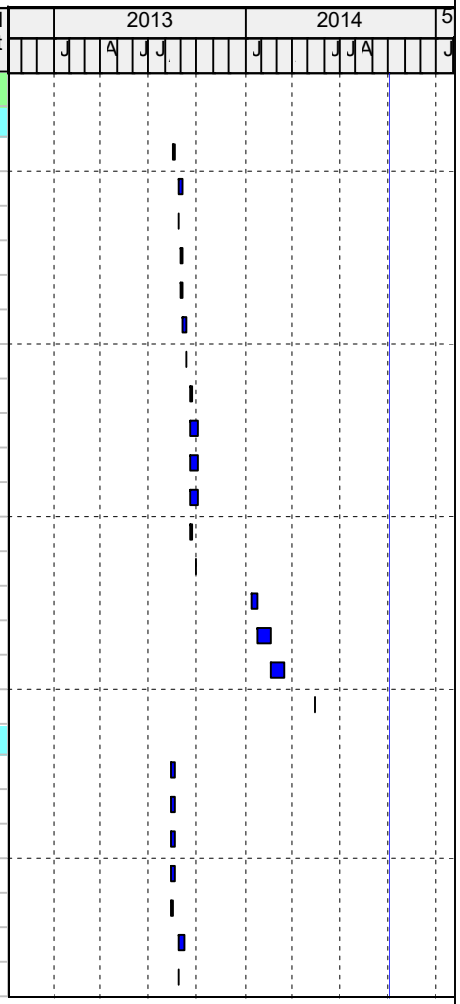



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2023 | LL2 - Waterproof Walls | 3 | 0 | 29-Aug-13 A | 03-Sep-13 A | |
| LL2-2014 | LL2 - Stress Tendons | 1 | 0 | 30-Aug-13 A | 30-Aug-13 A | |
| LL2-2016 | LL2 - Strip / ReShore | 3 | 0 | 03-Sep-13 A | 05-Sep-13 A | |
| LL2-8234 | LL2 - Place / Finish Deck | 3 | 0 | 12-Sep-13 A | 12-Sep-13 A | |
| LL2-2000 | LL2 - FRP Core Walls | 8 | 0 | 12-Sep-13 A | 23-Sep-13 A | |
| LL2-2018 | LL2 - Remove ReShores | 4 | 0 | 13-Nov-13 A | 18-Nov-13 A | |
| LL2-2013 | LL2 - F/R/P Pour #1 | 4 | 0 | 13-Jan-14 A | 16-Jan-14 A | |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| P5A-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2000 | LL1 - FRP Core Walls | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2004 | LL1 - Shore / Form Deck | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| P6-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P6-2004 | LL1 - Shore / Form Deck | 7 | 0 | 16-Sep-13 A | 24-Sep-13 A | |
| P5A-2006 | LL1 - MEP Rough In | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2008 | LL1 - ReSteel / PT Cables | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2012 | LL1 - Place / Finish Deck | 0 | 0 | 20-Sep-13 A | | |
| P5A-2020 | LL1 - Waterproof Walls | 3 | 0 | 20-Sep-13 A | 24-Sep-13 A | |
| P5A-2014 | LL1 - Stress Tendons | 1 | 0 | 23-Sep-13 A | 23-Sep-13 A | |
| P5A-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2006 | LL1 - MEP Rough In | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2008 | LL1 - ReSteel / PT Cables | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 24-Sep-13 A | 25-Sep-13 A | |
| P6-2020 | LL1 - Waterproof Walls | 4 | 0 | 24-Sep-13 A | 27-Sep-13 A | |
| P5A-2033 | LL1 - Resteel/Shotcrete Walls | 3 | 0 | 25-Sep-13 A | 27-Sep-13 A | |
| P5B-2002 | LL1 - FRP Columns Below | 5 | 0 | 26-Sep-13 A | 02-Oct-13 A | |
| P5B-2004 | LL1 - Shore / Form Deck | 7 | 0 | 26-Sep-13 A | 04-Oct-13 A | |

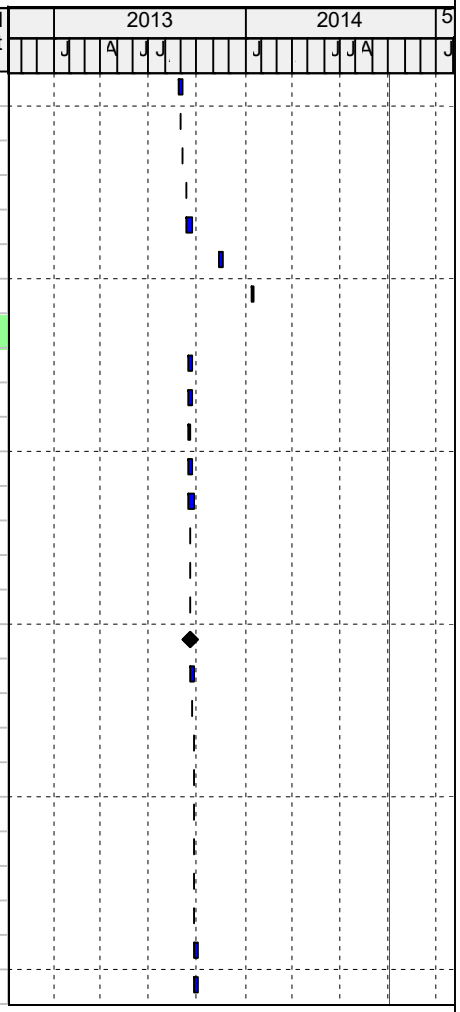



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P6-2012 | LL1 - Place / Finish Deck | 0 | 0 | 27-Sep-13 A | | |
| P6-2014 | LL1 - Stress Tendons | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2033 | LL1 - Resteel/Shotcrete Walls | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 01-Oct-13 A | 03-Oct-13 A | |
| P5B-2006 | LL1 - MEP Rough In | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2002 | FRP Columns Below | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2004 | Shore / Form Deck | 4 | 0 | 03-Oct-13 A | 08-Oct-13 A | |
| P5B-2008 | LL1 - ReSteel / PT Cables | 5 | 0 | 04-Oct-13 A | 10-Oct-13 A | |
| P5B-2010 | LL1 - Install Edgeform/Embeds | 4 | 0 | 04-Oct-13 A | 09-Oct-13 A | |
| P8-2002 | FRP Columns Below | 5 | 0 | 07-Oct-13 A | 11-Oct-13 A | |
| P8-2000 | Form/Resteel/Close Core Walls | 14 | 0 | 07-Oct-13 A | 24-Oct-13 A | |
| P8-2004 | Shore / Form Deck P8 | 8 | 0 | 07-Oct-13 A | 16-Oct-13 A | |
| P7-2002 | FRP Columns Below | 5 | 0 | 08-Oct-13 A | 14-Oct-13 A | |
| P7-2004 | Shore / Form Deck | 6 | 0 | 08-Oct-13 A | 15-Oct-13 A | |
| P10A--2006 | MEP Rough In | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2008 | ReSteel / PT Cables | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2010 | Install Edgeform/Embeds | 2 | 0 | 08-Oct-13 A | 09-Oct-13 A | |
| P5B-2012 | LL1 - Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P10A--2012 | Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P5B-2014 | LL1 - Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P7-2006 | MEP Rough In | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P7-2008 | ReSteel / PT Cables | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P10A--2014 | Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P8-2020 | Shore / Form Deck P9 | 6 | 0 | 14-Oct-13 A | 21-Oct-13 A | |
| P5B-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2010 | Install Edgeform/Embeds | 2 | 0 | 15-Oct-13 A | 16-Oct-13 A | |
| P8-2006 | MEP Rough In | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |

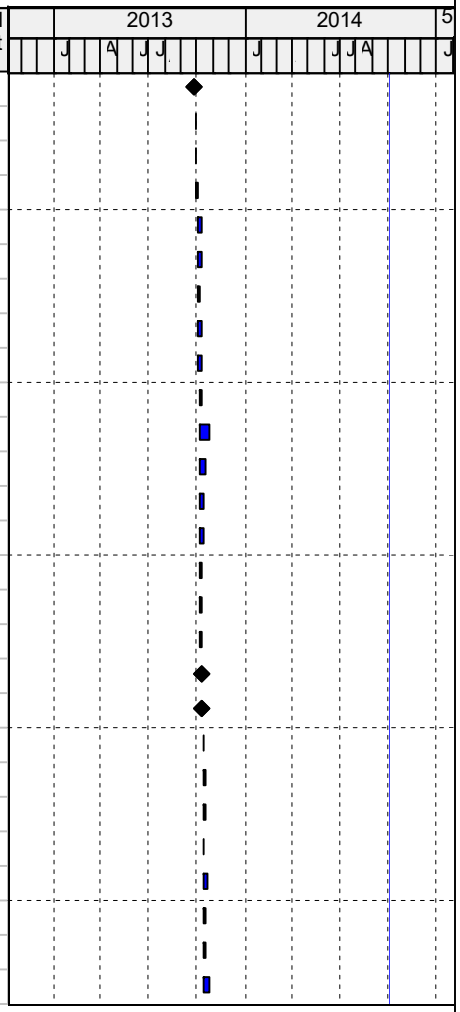



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P8-2008 | ReSteel / PT Cables | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2010 | Install Edgeform/Embeds | 4 | 0 | 15-Oct-13 A | 18-Oct-13 A | |
| P10A--2016 | Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2012 | Place / Finish Deck | 0 | 0 | 18-Oct-13 A | | |
| P7-2033 | Resteel/Shotcrete Walls | 3 | 0 | 18-Oct-13 A | 22-Oct-13 A | |
| P7-2014 | Stress Tendons | 1 | 0 | 21-Oct-13 A | 21-Oct-13 A | |
| P7-2016 | Strip / ReShore Deck | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2002 | FRP Columns Below | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P10B--2000 | FRP Shear Walls Below | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2004 | Shore / Form Deck | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P8-2012 | Place / Finish Deck P 8 & 9 and Core Walls | 0 | 0 | 25-Oct-13 A | | |
| P8-2014 | Stress Tendons | 1 | 0 | 28-Oct-13 A | 28-Oct-13 A | |
| P10B--2006 | MEP Rough In | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2008 | ReSteel / PT Cables | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2010 | Install Edgeform/Embeds | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P12--2002 | FRP Columns Below | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P12--2000 | Form/Resteel/Close Core Walls | 9 | 0 | 28-Oct-13 A | 07-Nov-13 A | |
| P12--2004 | Shore / Form Deck | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P8-2016 | Strip / ReShore Deck | 3 | 0 | 29-Oct-13 A | 31-Oct-13 A | |
| P11--2002 | FRP Columns Below | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P11--2004 | Shore / Form Deck | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P10B--2012 | Place / Finish Deck | 0 | 0 | 31-Oct-13 A | | |
| P10B--2014 | Stress Tendons | 1 | 0 | 01-Nov-13 A | 01-Nov-13 A | |
| P12--2006 | MEP Rough In | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12--2008 | ReSteel / PT Cables | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12--2010 | Install Edgeform/Embeds | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P10B--2016 | Strip / ReShore Deck | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |

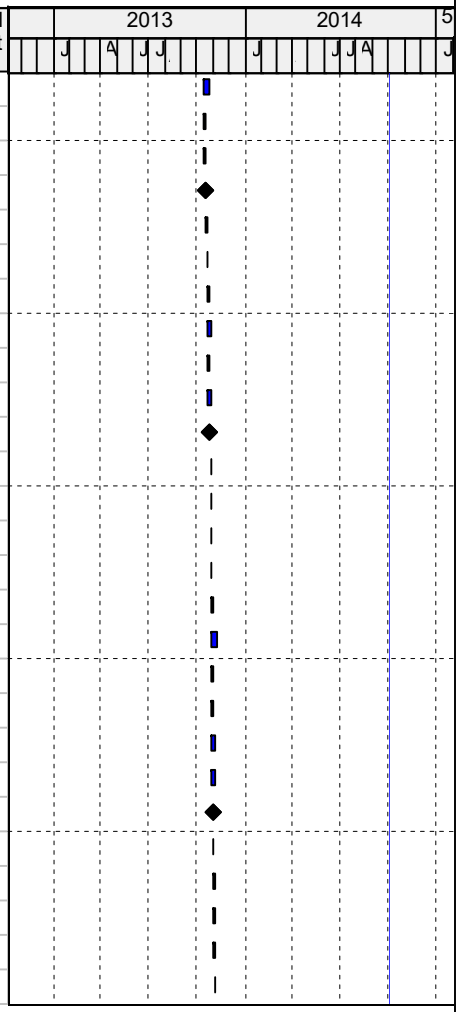



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P11–2006 | MEP Rough In | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2008 | ReSteel / PT Cables | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2010 | Install Edgeform/Embeds | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2012 | Place / Finish Deck | 0 | 0 | 07-Nov-13 A | | |
| P13–2002 | FRP Columns Below | 5 | 0 | 07-Nov-13 A | 14-Nov-13 A | |
| P13–2004 | Shore / Form Deck | 9 | 0 | 07-Nov-13 A | 28-Nov-13 A | |
| P11–2014 | Stress Tendons | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| P12–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 08-Nov-13 A | | |
| P11–2016 | Strip / ReShore Deck | 3 | 0 | 12-Nov-13 A | 14-Nov-13 A | |
| P12–2014 | Stress Tendons | 1 | 0 | 12-Nov-13 A | 12-Nov-13 A | |
| P14–2002 | FRP Columns Below | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P14–2000 | Form/Resteel/Close Core Walls | 8 | 0 | 19-Nov-13 A | 03-Dec-13 A | |
| P14–2004 | Shore / Form Deck | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P13A–2002 | FRP Columns Below | 5 | 0 | 21-Nov-13 A | 27-Nov-13 A | |
| P13A–2004 | Shore / Form Deck | 4 | 0 | 21-Nov-13 A | 26-Nov-13 A | |
| P13–2010 | Install Edgeform/Embeds | 5 | 0 | 22-Nov-13 A | 04-Dec-13 A | |
| P13–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2006 | MEP Rough In | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2010 | Install Edgeform/Embeds | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P13–2006 | MEP Rough In | 5 | 0 | 26-Nov-13 A | 03-Dec-13 A | |
| P13A–2006 | MEP Rough In | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2008 | ReSteel / PT Cables | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2010 | Install Edgeform/Embeds | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13–2012 | Place / Finish Deck | 0 | 0 | 02-Dec-13 A | | |
| P13A–2012 | Place / Finish Deck | 0 | 0 | 03-Dec-13 A | | |
| P14–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 04-Dec-13 A | | |

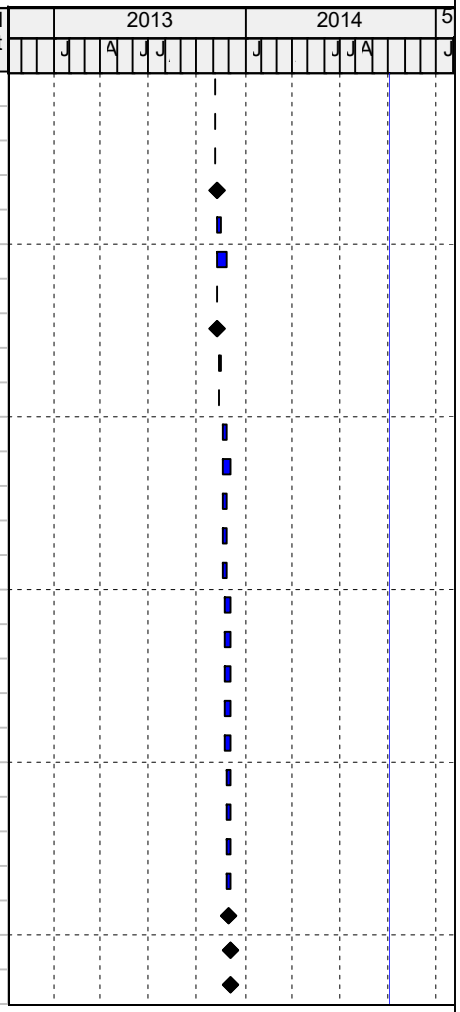



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P13–2014 | Stress Tendons | 1 | 0 | 05-Dec-13 A | 05-Dec-13 A | |
| P15–2002 | FRP Columns Below | 3 | 0 | 05-Dec-13 A | 09-Dec-13 A | |
| P15–2000 | Jump/Resteel/Close Core | 9 | 0 | 05-Dec-13 A | 17-Dec-13 A | |
| P15–2004 | Shore / Form Deck | 5 | 0 | 05-Dec-13 A | 11-Dec-13 A | |
| P13–2016 | Strip / ReShore Deck | 3 | 0 | 06-Dec-13 A | 10-Dec-13 A | |
| P13A–2014 | Stress Tendons | 1 | 0 | 06-Dec-13 A | 06-Dec-13 A | |
| P14–2014 | Stress Tendons | 1 | 0 | 07-Dec-13 A | 07-Dec-13 A | |
| P15–2006 | MEP Rough In | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2008 | ReSteel / PT Cables | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2010 | Install Edgeform/Embeds | 3 | 0 | 11-Dec-13 A | 13-Dec-13 A | |
| P16-2002 | FRP Columns Below | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P16-2004 | Shore / Form Deck | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P15–2012 | Place / Finish Deck | 0 | 0 | 18-Dec-13 A | | |
| P15–2020 | Place Conc @ Core | 0 | 0 | 18-Dec-13 A | | |
| P16-2000 | Jump/Resteel/Close Core | 5 | 0 | 18-Dec-13 A | 24-Dec-13 A | |
| P16-2006 | MEP Rough In | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2008 | ReSteel / PT Cables | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2010 | Install Edgeform/Embeds | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P15–2014 | Stress Tendons | 1 | 0 | 21-Dec-13 A | 21-Dec-13 A | |
| P8-2018 | Remove Reshores | 2 | 0 | 23-Dec-13 A | 24-Dec-13 A | |
| P10A–2018 | Remove Reshores | 2 | 0 | 26-Dec-13 A | 27-Dec-13 A | |
| P16-2012 | Place / Finish Deck | 0 | 0 | 26-Dec-13 A | | |
| P16-2020 | Place Conc @ Core | 0 | 0 | 26-Dec-13 A | | |
| P17-2002 | FRP Columns Below | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P17-2000 | Jump/Resteel/Close Core | 7 | 0 | 27-Dec-13 A | 07-Jan-14 A | |
| P17-2004 | Shore / Form Deck | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P10B–2018 | Remove Reshores | 2 | 0 | 30-Dec-13 A | 31-Dec-13 A | |

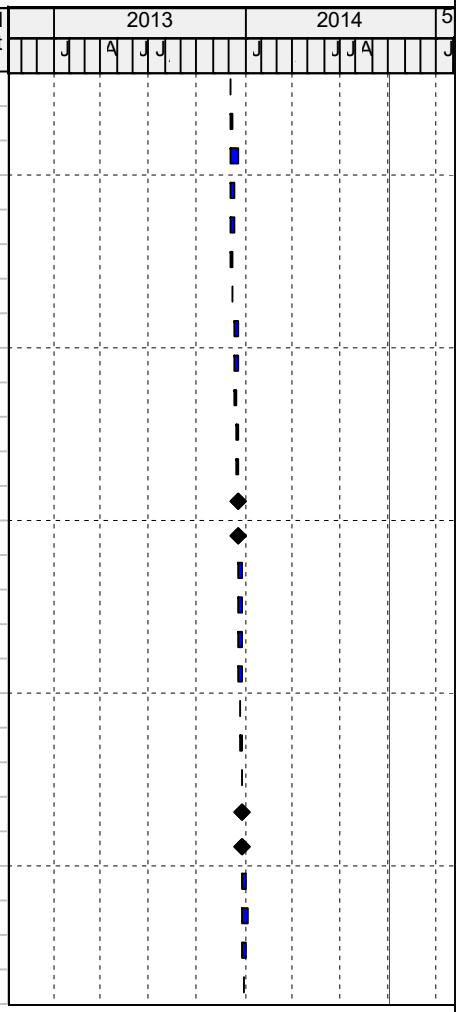



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P16-2014 | Stress Tendons | 1 | 0 | 31-Dec-13 A | 31-Dec-13 A | |
| P5A-2018 | LL1 - Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P11–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P12–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P17-2006 | MEP Rough In | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2008 | ReSteel / PT Cables | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2010 | Install Edgeform/Embeds | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P6-2018 | LL1 - Remove Reshores | 2 | 0 | 06-Jan-14 A | 07-Jan-14 A | |
| P5B-2018 | LL1 - Remove Reshores | 2 | 0 | 08-Jan-14 A | 09-Jan-14 A | |
| P17-2012 | Place / Finish Deck | 0 | 0 | 08-Jan-14 A | | |
| P17-2020 | Place Conc @ Core | 0 | 0 | 08-Jan-14 A | | |
| P18-2002 | FRP Columns Below | 5 | 0 | 09-Jan-14 A | 15-Jan-14 A | |
| P18-2000 | Jump/Resteel/Close Core | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P18-2004 | Shore / Form Deck | 3 | 0 | 09-Jan-14 A | 13-Jan-14 A | |
| LL2-2022R | MEP Rough In | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P7-2018 | Remove Reshores | 2 | 0 | 10-Jan-14 A | 13-Jan-14 A | |
| P17-2014 | Stress Tendons | 1 | 0 | 11-Jan-14 A | 11-Jan-14 A | |
| P13–2018 | Remove Reshores | 2 | 0 | 13-Jan-14 A | 14-Jan-14 A | |
| P13A–2018 | Remove Reshores | 2 | 0 | 15-Jan-14 A | 16-Jan-14 A | |
| WEA-2012 | WIND IMPACT | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| P18-2006 | MEP Rough In | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2008 | ReSteel / PT Cables | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2010 | Install Edgeform/Embeds | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2012 | Place / Finish Deck | 0 | 0 | 22-Jan-14 A | | |
| P18-2020 | Place Conc @ Core | 0 | 0 | 22-Jan-14 A | | |
| P19-2002 | FRP Columns Below | 5 | 0 | 23-Jan-14 A | 29-Jan-14 A | |
| P19-2000 | Jump/Resteel/Close Core | 4 | 0 | 23-Jan-14 A | 28-Jan-14 A | |

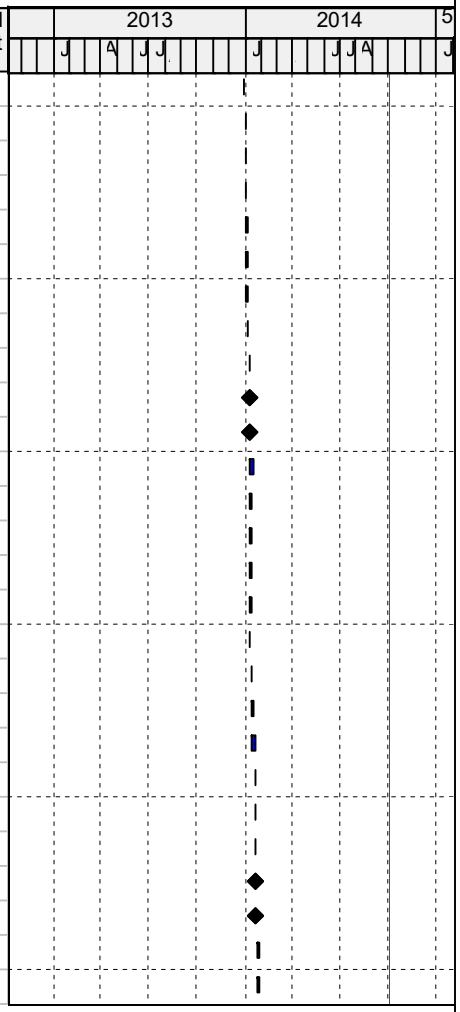



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P19-2004 | Shore / Form Deck | 3 | 0 | 23-Jan-14 A | 27-Jan-14 A | |
| P18-2014 | Stress Tendons | 1 | 0 | 25-Jan-14 A | 25-Jan-14 A | |
| P14–2018 | Remove Reshores | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2006 | MEP Rough In | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2008 | ReSteel / PT Cables | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2010 | Install Edgeform/Embeds | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2012 | Place / Finish Deck | 0 | 0 | 29-Jan-14 A | | |
| P19-2020 | Place Conc @ Core | 0 | 0 | 29-Jan-14 A | | |
| P20-2002 | FRP Columns Below | 5 | 0 | 30-Jan-14 A | 05-Feb-14 A | |
| P20-2000 | Jump/Resteel/Close Core | 9 | 0 | 30-Jan-14 A | 11-Feb-14 A | |
| P20-2004 | Shore / Form Deck | 6 | 0 | 30-Jan-14 A | 10-Feb-14 A | |
| P19-2014 | Stress Tendons | 1 | 0 | 01-Feb-14 A | 01-Feb-14 A | |
| P13A–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P14–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P15–2016 | Strip / ReShore Deck | 3 | 0 | 06-Feb-14 A | 10-Feb-14 A | |
| P20-2006 | MEP Rough In | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2008 | ReSteel / PT Cables | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2010 | Install Edgeform/Embeds | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| L03-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 06-Feb-14 A | 12-Feb-14 A | |
| P16-2016 | Strip / ReShore Deck | 3 | 0 | 10-Feb-14 A | 12-Feb-14 A | |
| L04-2018 | Remove Reshores | 2 | 0 | 10-Feb-14 A | 11-Feb-14 A | |
| L03-2018 | Remove Reshores | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| P17-2016 | Strip / ReShore Deck | 3 | 0 | 12-Feb-14 A | 14-Feb-14 A | |
| P20-2012 | Place / Finish Deck | 0 | 0 | 12-Feb-14 A | | |
| P20-2020 | Place Conc @ Core | 0 | 0 | 12-Feb-14 A | | |
| L04-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-Feb-14 A | 18-Feb-14 A | |
| P12–2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |

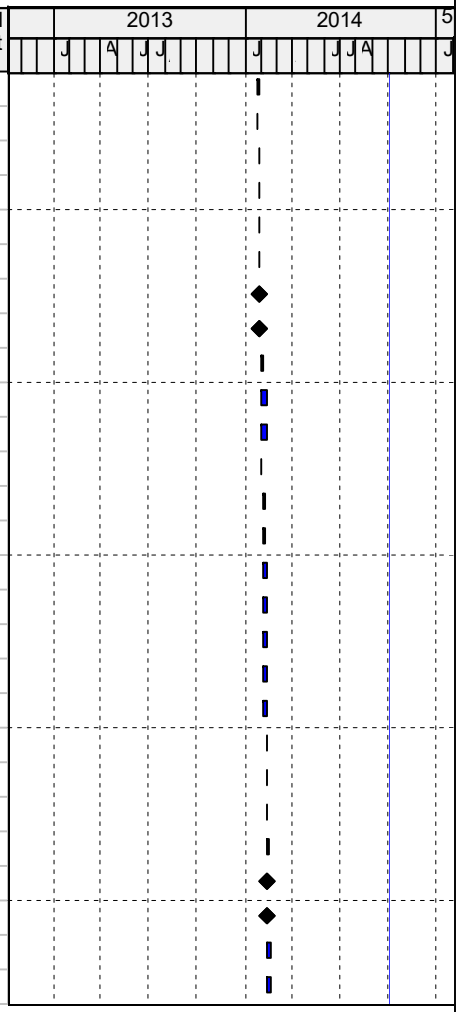


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P18-2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P21-2002 | FRP Columns Below | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| P21-2000 | Jump/Resteel/Close Core | 4 | 0 | 13-Feb-14 A | 18-Feb-14 A | |
| P21-2004 | Shore / Form Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P19-2016 | Strip / ReShore Deck | 3 | 0 | 14-Feb-14 A | 18-Feb-14 A | |
| P20-2014 | Stress Tendons | 1 | 0 | 15-Feb-14 A | 15-Feb-14 A | |
| P21-2006 | MEP Rough In | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2008 | ReSteel / PT Cables | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P20-2016 | Strip / ReShore Deck | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| L05-2018 | Remove Reshores | 2 | 0 | 18-Feb-14 A | 19-Feb-14 A | |
| P21-2012 | Place / Finish Deck | 0 | 0 | 19-Feb-14 A | | |
| P21-2020 | Place Conc @ Core | 0 | 0 | 19-Feb-14 A | | |
| P22-2002 | FRP Columns Below | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P22-2000 | Jump/Resteel/Close Core | 4 | 0 | 20-Feb-14 A | 25-Feb-14 A | |
| P22-2004 | Shore / Form Deck | 3 | 0 | 20-Feb-14 A | 24-Feb-14 A | |
| L05-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P21-2014 | Stress Tendons | 1 | 0 | 22-Feb-14 A | 22-Feb-14 A | |
| P21-2016 | Strip / ReShore Deck | 3 | 0 | 24-Feb-14 A | 26-Feb-14 A | |
| P22-2006 | MEP Rough In | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2008 | ReSteel / PT Cables | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| L06-2018 | Remove Reshores | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| P22-2012 | Place / Finish Deck | 0 | 0 | 26-Feb-14 A | | |
| P22-2020 | Place Conc @ Core | 0 | 0 | 26-Feb-14 A | | |
| P23-2002 | FRP Columns Below | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2000 | Jump/Resteel/Close Core | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |

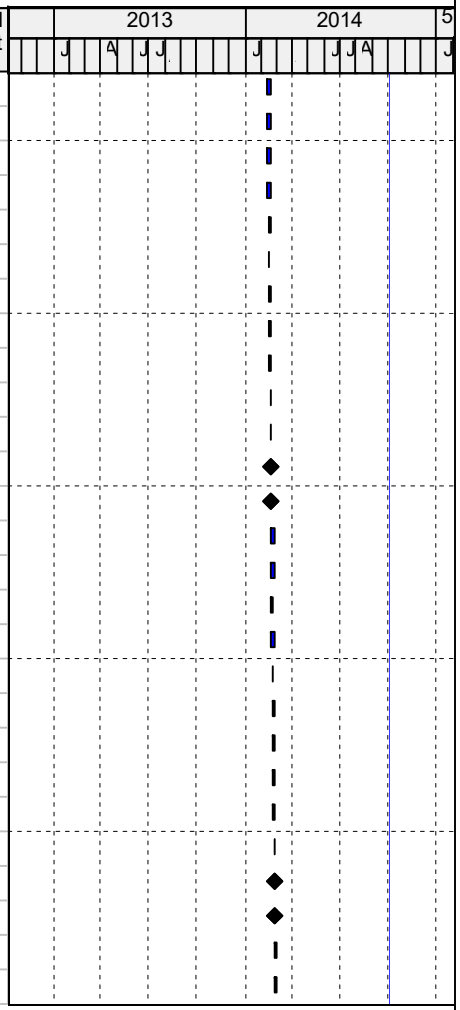



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P23-2004 | Shore / Form Deck | 3 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2006 | MEP Rough In | 2 | 0 | 01-Mar-14 A | 03-Mar-14 A | |
| P22-2014 | Stress Tendons | 1 | 0 | 01-Mar-14 A | 01-Mar-14 A | |
| P23-2008 | ReSteel / PT Cables | 2 | 0 | 03-Mar-14 A | 04-Mar-14 A | |
| P22-2016 | Strip / ReShore Deck | 3 | 0 | 04-Mar-14 A | 10-Mar-14 A | |
| P23-2010 | Install Edgeform/Embeds | 2 | 0 | 04-Mar-14 A | 04-Mar-14 A | |
| L07-2018 | Remove Reshores | 2 | 0 | 04-Mar-14 A | 05-Mar-14 A | |
| P23-2012 | Place / Finish Deck | 0 | 0 | 05-Mar-14 A | | |
| P23-2020 | Place Conc @ Core | 0 | 0 | 05-Mar-14 A | | |
| P24-2002 | FRP Columns Below | 5 | 0 | 05-Mar-14 A | 07-Mar-14 A | |
| P24-2004 | Shore / Form Deck | 3 | 0 | 06-Mar-14 A | 10-Mar-14 A | |
| P24-2000 | Jump/Resteel/Close Core | 4 | 0 | 08-Mar-14 A | 10-Mar-14 A | |
| P23-2014 | Stress Tendons | 1 | 0 | 10-Mar-14 A | 10-Mar-14 A | |
| P24-2008 | ReSteel / PT Cables | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P24-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P23-2016 | Strip / ReShore Deck | 3 | 0 | 11-Mar-14 A | 17-Mar-14 A | |
| P24-2006 | MEP Rough In | 2 | 0 | 11-Mar-14 A | 11-Mar-14 A | |
| P25-2002 | FRP Columns Below | 5 | 0 | 11-Mar-14 A | 13-Mar-14 A | |
| L08-2018 | Remove Reshores | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| P24-2012 | Place / Finish Deck | 0 | 0 | 12-Mar-14 A | | |
| P24-2020 | Place Conc @ Core | 0 | 0 | 12-Mar-14 A | | |
| P25-2004 | Shore / Form Deck | 3 | 0 | 13-Mar-14 A | 17-Mar-14 A | |
| P25-2000 | Jump/Resteel/Close Core | 4 | 0 | 15-Mar-14 A | 17-Mar-14 A | |
| P24-2014 | Stress Tendons | 1 | 0 | 17-Mar-14 A | 17-Mar-14 A | |
| P25-2006 | MEP Rough In | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2008 | ReSteel / PT Cables | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |

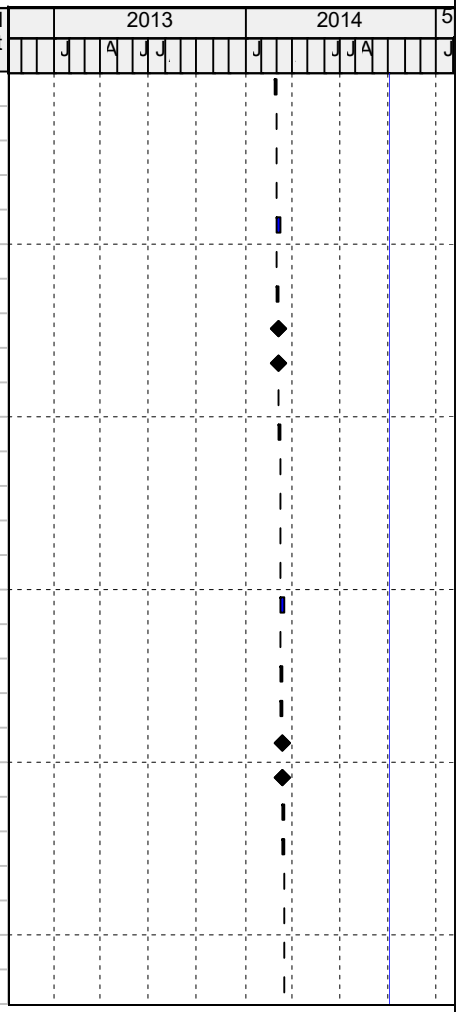


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 18-Mar-14 A | 20-Mar-14 A | |
| L09-2018 | Remove Reshores | 2 | 0 | 18-Mar-14 A | 19-Mar-14 A | |
| P26-2002 | FRP Columns Below | 5 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| P25-2012 | Place / Finish Deck | 0 | 0 | 19-Mar-14 A | | |
| P25-2020 | Place Conc @ Core | 0 | 0 | 19-Mar-14 A | | |
| P26-2004 | Shore / Form Deck | 3 | 0 | 20-Mar-14 A | 24-Mar-14 A | |
| L07-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 21-Mar-14 A | 25-Mar-14 A | |
| P26-2000 | Jump/Resteel/Close Core | 4 | 0 | 22-Mar-14 A | 24-Mar-14 A | |
| P26-2006 | MEP Rough In | 2 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P26-2008 | ReSteel / PT Cables | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P26-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P25-2014 | Stress Tendons | 1 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P27-2002 | FRP Columns Below | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| P26-2012 | Place / Finish Deck | 0 | 0 | 26-Mar-14 A | | |
| P26-2020 | Place Conc @ Core | 0 | 0 | 26-Mar-14 A | | |
| L08-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 26-Mar-14 A | 28-Mar-14 A | |
| L10-2018 | Remove Reshores | 2 | 0 | 26-Mar-14 A | 27-Mar-14 A | |
| P27-2004 | Shore / Form Deck | 3 | 0 | 27-Mar-14 A | 31-Mar-14 A | |
| P27-2000 | Jump/Resteel/Close Core | 4 | 0 | 29-Mar-14 A | 31-Mar-14 A | |
| P27-2006 | MEP Rough In | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2008 | ReSteel / PT Cables | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2010 | Install Edgeform/Embeds | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P26-2014 | Stress Tendons | 1 | 0 | 31-Mar-14 A | 31-Mar-14 A | |
| L09-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 31-Mar-14 A | 02-Apr-14 A | |
| P24-2016 | Strip / ReShore Deck | 3 | 0 | 01-Apr-14 A | 07-Apr-14 A | |
| L11-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 02-Apr-14 A | |
| L12-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 03-Apr-14 A | |

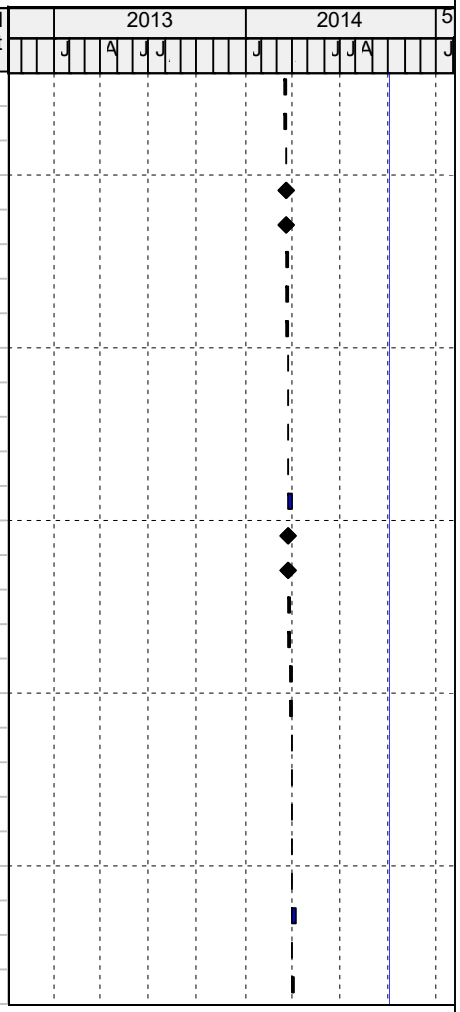


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P27-2012 | Place / Finish Deck | 0 | 0 | 02-Apr-14 A | | |
| P27-2020 | Place Conc @ Core | 0 | 0 | 02-Apr-14 A | | |
| P28-2002 | FRP Columns Below | 5 | 0 | 02-Apr-14 A | 04-Apr-14 A | |
| P28-2004 | Shore / Form Deck | 4 | 0 | 03-Apr-14 A | 08-Apr-14 A | |
| L10-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| P27-2014 | Stress Tendons | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| P25-2016 | Strip / ReShore Deck | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L14-2018 | Remove Reshores | 2 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| P28-2000 | Jump/Resteel/Close Core | 7 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| P28-2006 | MEP Rough In | 4 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2008 | ReSteel / PT Cables | 4 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Apr-14 A | 11-Apr-14 A | |
| L12-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| P28-2012 | Place / Finish Deck | 0 | 0 | 14-Apr-14 A | | |
| P28-2020 | Place Conc @ Core | 0 | 0 | 14-Apr-14 A | | |
| P29-2002 | FRP Columns Above Roof Deck | 3 | 0 | 14-Apr-14 A | 18-Apr-14 A | |
| P26-2016 | Strip / ReShore Deck | 3 | 0 | 14-Apr-14 A | 17-Apr-14 A | |
| L14-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-Apr-14 A | 18-Apr-14 A | |
| P28-2014 | Stress Tendons | 1 | 0 | 17-Apr-14 A | 17-Apr-14 A | |
| P29-2000 | Strip Core | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| P27-2016 | Strip / ReShore Deck | 3 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L15-2018 | Remove Reshores | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| P28-2016 | Strip / ReShore Deck | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L15-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L16-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-May-14 A | 19-May-14 A | |
| L16-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |

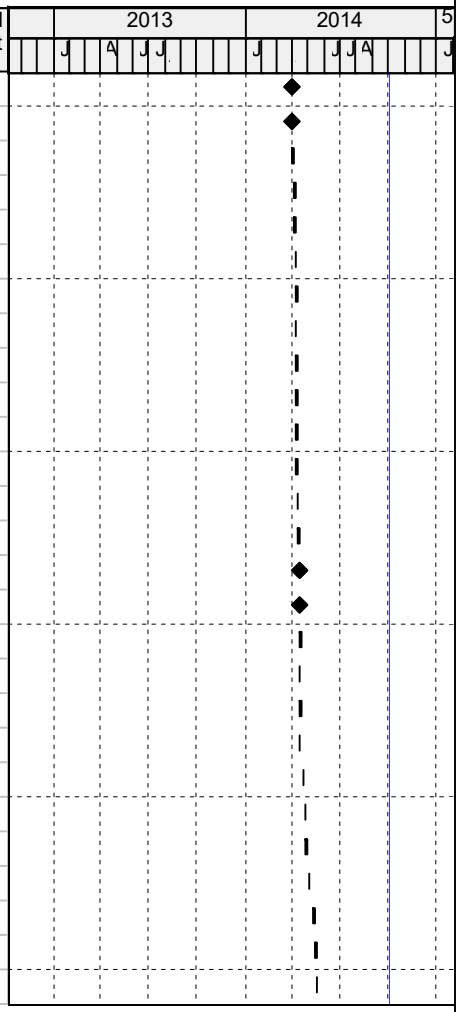



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2019 | Grind Ceiling for Skim Coat | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| **Ballroom Catwalk & Roof** | | | | | | |
| PC-2100 | Erect Structural Steel @ Porte Cochere | 3 | 0 | 30-Jan-14 A | 03-Feb-14 A | |
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 7 | 0 | 07-Feb-14 A | 17-Feb-14 A | |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| PC-2102 | Metal Decking @ Porte Cochere/ Roof | 2 | 0 | 17-Apr-14 A | 18-Apr-14 A | |
| BR-2112 | BR - Fireproofing @ Structural Steel | 2 | 0 | 27-May-14 A | 30-May-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Mech Penthouse** | | | | | | |
| PH-8706 | Set Mech Equipment @ Tower Roof | 3 | 0 | 22-May-14 A | 28-May-14 A | |
| PH-8708 | Set Equipment @ Penthouse | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| PH-8700 | PH - Structural Steel and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| **Vertical Circulation** | | | | | | |
| **Stairs** | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 25-Nov-13 A | 26-Nov-13 A | |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 27-Nov-13 A | 03-Dec-13 A | |
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 04-Dec-13 A | 05-Dec-13 A | |
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 06-Dec-13 A | 09-Dec-13 A | |
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 2 | 0 | 03-Feb-14 A | 04-Feb-14 A | |
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 2 | 0 | 06-Feb-14 A | 07-Feb-14 A | |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 2 | 0 | 07-Feb-14 A | 07-Feb-14 A | |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 2 | 0 | 07-Feb-14 A | 10-Feb-14 A | |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 2 | 0 | 10-Feb-14 A | 10-Feb-14 A | |

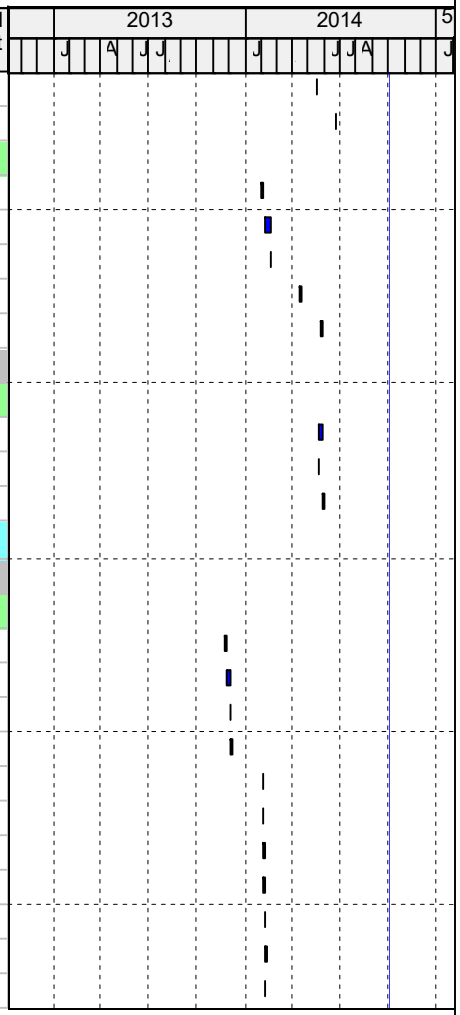



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 2 | 0 | 06-Mar-14 A | 07-Mar-14 A | |
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 2 | 0 | 07-Mar-14 A | 10-Mar-14 A | |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 2 | 0 | 13-Mar-14 A | 14-Mar-14 A | |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 2 | 0 | 08-Apr-14 A | 21-Apr-14 A | |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| S1-4040 | Stair 1 - Set Mtl Stairs / Railings L18 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 10-Dec-13 A | 11-Dec-13 A | |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 12-Dec-13 A | 13-Dec-13 A | |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 16-Dec-13 A | 17-Dec-13 A | |
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 18-Dec-13 A | 19-Dec-13 A | |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 2 | 0 | 12-Feb-14 A | 13-Feb-14 A | |
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 2 | 0 | 13-Feb-14 A | 13-Feb-14 A | |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 2 | 0 | 13-Feb-14 A | 14-Feb-14 A | |
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 2 | 0 | 19-Feb-14 A | 20-Feb-14 A | |
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 2 | 0 | 21-Feb-14 A | 24-Feb-14 A | |
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 2 | 0 | 19-Mar-14 A | 20-Mar-14 A | |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 2 | 0 | 21-Mar-14 A | 22-Mar-14 A | |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |

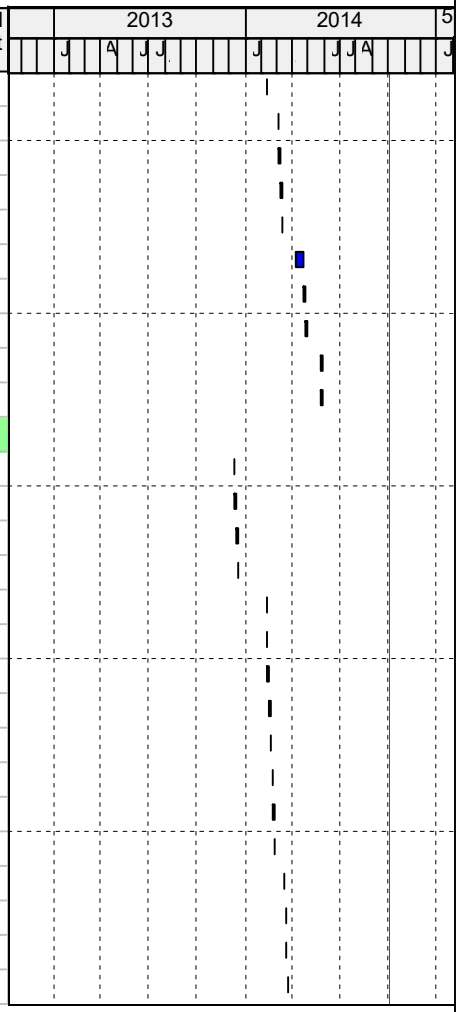



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 2 | 0 | 14-May-14 A | 15-May-14 A | |
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 2 | 0 | 16-May-14 A | 19-May-14 A | |
| S2-4038 | Stair 2 - Set Mtl Stairs / Railings L17 | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - Set Metal Stairs / Railings LL2 | 6 | 0 | 05-Mar-14 A | 20-Mar-14 A | |
| S3-4002 | Stair 3 - Set Metal Stairs / Railings LL1 | 6 | 0 | 17-Mar-14 A | 21-Mar-14 A | |
| S3-4004 | Stair 3 - Permanent Railings / Final Finishes | 4 | 4 | 01-Dec-14 | 04-Dec-14 | 27 |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |
| S4-4000 | Stair 4 - Set Metal Stairs / Railings LL2 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4002 | Stair 4 - Set Metal Stairs / Railings LL1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4004 | Stair 4 -Set Metal Stairs / Railings L1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4006 | Stair 4 - Permanent Railings / Final Finishes | 4 | 4 | 05-Dec-14 | 10-Dec-14 | 21 |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |
| S6-4000 | Stair 6 - Set Metal Stairs / Railings | 5 | 0 | 25-Jun-14 A | 01-Jul-14 A | |
| S6-4002 | Stair 6 - Permanent Railings / Final Finishes | 2 | 2 | 19-Nov-14 | 20-Nov-14 | 35 |
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes | 5 | 5 | 29-Dec-14 | 05-Jan-15 | 8 |
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a -Set Metal Stairs / Railings L1 | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| S4a-4002 | Stair 4a - Permanent Railings / Final Finishes | 2 | 2 | 11-Dec-14 | 12-Dec-14 | 21 |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 07-Jun-13 A | | |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 0 | 17-Jun-13 A | 21-Jun-13 A | |

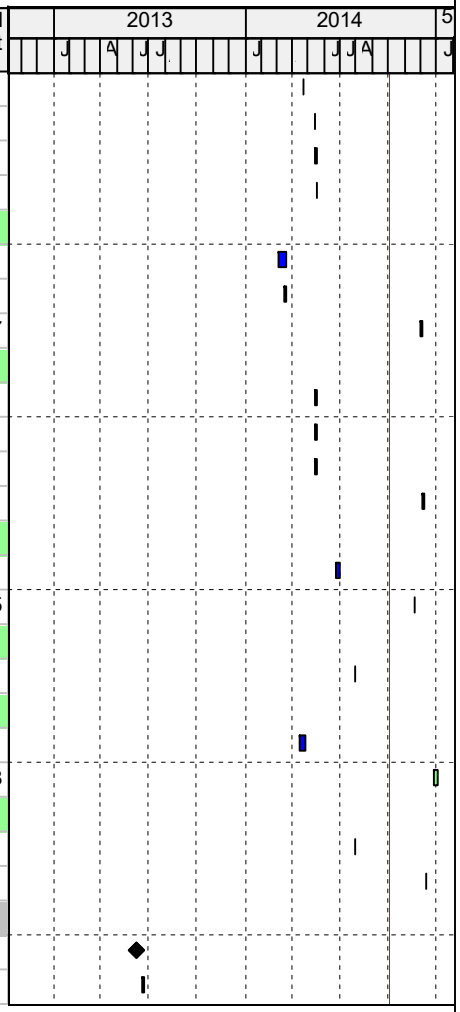



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-1004 | Elev - Submittal Approval | 21 | 0 | 21-Jun-13 A | 01-Jan-14 A | |
| EL-1006 | Elev - Release to Manufacturing | 14 | 0 | 02-Jan-14 A | 15-Jan-14 A | |
| EL-1008 | Elev - Fabrication (Engineered Geared) | 95 | 0 | 16-Jan-14 A | 14-Jun-14 A | |
| EL-1010 | Elev - Machines delivered | 1 | 0 | 12-May-14 A | 12-May-14 A | |
| EL-1011 | Elev - Elevator Machines Flown & Set At Top Of Hoist | 5 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5016 | Elev 5 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-1216 | Elev 1&2 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-3416 | Elev 3&4 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-1202 | Elev 1&2 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-3402 | Elev 3&4 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-5018 | Elev 5 - Set Hoistway Machines | 3 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| EL-1218 | Elev 1&2 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-3418 | Elev 3&4 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-1200 | Elev 1&2 - Hoistway Clear & Ready (GC) | 0 | 0 | 20-Jun-14 A | | |
| EL-1204 | Elev 1&2 - Install Rails & Brackets | 17 | 0 | 23-Jun-14 A | 15-Jul-14 A | |
| EL-3400 | Elev 3&4 - Hoistway Clear & Ready (GC) | 0 | 0 | 23-Jun-14 A | | |
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 24-Jun-14 A | | |
| EL-1206 | Elev 1&2 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Jul-14 A | |
| EL-1207 | Elev 1&2 - Install Pit Equipment/Car Sling/CWT Fram | 3 | 0 | 15-Jul-14 A | 01-Aug-14 A | |
| EL-1208 | Elev 1&2 - Install MHoist & Cable | 5 | 0 | 16-Jul-14 A | 24-Jul-14 A | |
| EL-3407 | Elev 3&4 - Install Pit Equipment/Car Sling/CWT Fram | 5 | 0 | 16-Jul-14 A | 06-Aug-14 A | |
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 21-Jul-14 A | | |
| EL-5004 | Elev 5 - Install Rails & Brackets | 13 | 0 | 21-Jul-14 A | 11-Aug-14 A | |
| EL-3404 | Elev 3&4 - Install Rails & Brackets | 18 | 0 | 23-Jul-14 A | 04-Aug-14 A | |
| EL-3406 | Elev 3&4 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 28-Jul-14 A | |

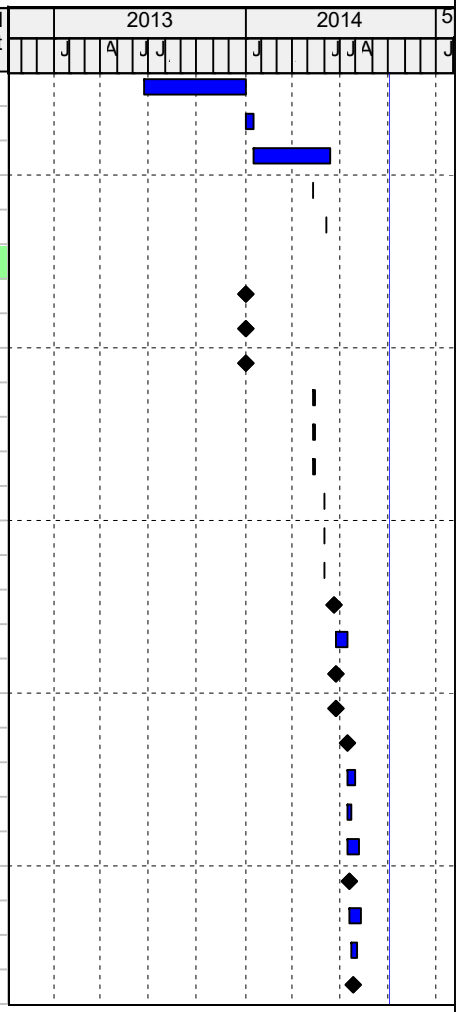


Actual Work | Remaining Work | Critical Remai... | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-3408 | Elev 3&4 - Install Hoist & Cable | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| EL-5007 | Elev 5 - Install Pit Equipment/Car Sling/CWT Frame/V | 5 | 0 | 12-Aug-14 A | 15-Aug-14 A | |
| EL-1210 | Elev 1&2 - Install Entrances/Doors/Fixtures/Fascia | 19 | 0 | 14-Aug-14 A | 22-Sep-14 A | |
| EL-3410 | Elev 3&4 - Install Entrances/Doors/Fixtures/Fascia | 30 | 0 | 14-Aug-14 A | 02-Oct-14 A | |
| EL-5006 | Elev 5 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Aug-14 A | |
| EL-5008 | Elev 5 - Install MHoist & Cable | 4 | 0 | 18-Aug-14 A | 20-Aug-14 A | |
| EL-5010 | Elev 5 - Install Entrances/Doors/Fixtures/Fascia | 21 | 0 | 21-Aug-14 A | 26-Sep-14 A | |
| EL-1212 | Elev 1&2 - Install Hoistway Equipment/Pipe & Wire | 14 | 6 | 22-Sep-14 A | 13-Oct-14 | 18 |
| EL-5012 | Elev 5 - Install Hoistway Equipment/Pipe & Wire | 14 | 9 | 26-Sep-14 A | 16-Oct-14 | 19 |
| EL-3412 | Elev 3&4 - Install Hoistway Equipment/Pipe & Wire | 23 | 21 | 03-Oct-14 A | 03-Nov-14 | 18 |
| EL-1214 | Elev 1&2 - Install Cab/Wiring/Door Operator(s) | 11 | 11 | 14-Oct-14 | 28-Oct-14 | 18 |
| EL-5014 | Elev 5 - Install Cab/Wiring/Door Operator(s) | 7 | 7 | 17-Oct-14 | 27-Oct-14 | 19 |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 1 | 1 | 24-Oct-14* | 24-Oct-14 | 17 |
| EL-6016 | Elev 6 - Hoistway Walls Complete (GC) | 0 | 0 | | 24-Oct-14 | 17 |
| EL-6004 | Elev 6 - Install Cylinders/Rails & Brackets | 4 | 4 | 27-Oct-14 | 30-Oct-14 | 17 |
| EL-5022 | Elev 5 - Adjust | 5 | 5 | 28-Oct-14 | 03-Nov-14 | 19 |
| EL-1222 | Elev 1&2 - Adjust | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 18 |
| EL-6006 | Elev 6 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 30-Oct-14 | 17 |
| EL-6007 | Elev 6 - Install Pit Equipment/Car Sling | 2 | 2 | 31-Oct-14 | 03-Nov-14 | 17 |
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 3 | 3 | 04-Nov-14 | 06-Nov-14 | 19 |
| EL-3414 | Elev 3&4 - Install Cab/Wiring/Door Operator(s) | 10 | 10 | 04-Nov-14 | 17-Nov-14 | 18 |
| EL-6018 | Elev 6 - Install Machine Room Equipment | 2 | 2 | 04-Nov-14 | 05-Nov-14 | 17 |
| EL-1224 | Elev 1&2 - Clean / Paint / Punchlist | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 18 |
| EL-6010 | Elev 6 - Install Entrances/Doors/Fixtures/Fascia | 3 | 3 | 06-Nov-14 | 10-Nov-14 | 17 |
| EL-5026 | Elev 5 - Inspections | 7 | 7 | 07-Nov-14 | 13-Nov-14 | 30 |
| EL-1226 | Elev 1&2 - Inspections | 7 | 7 | 08-Nov-14 | 14-Nov-14 | 29 |
| EL-6012 | Elev 6 - Install Hoistway Equipment/Pipe & Wire | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 17 |

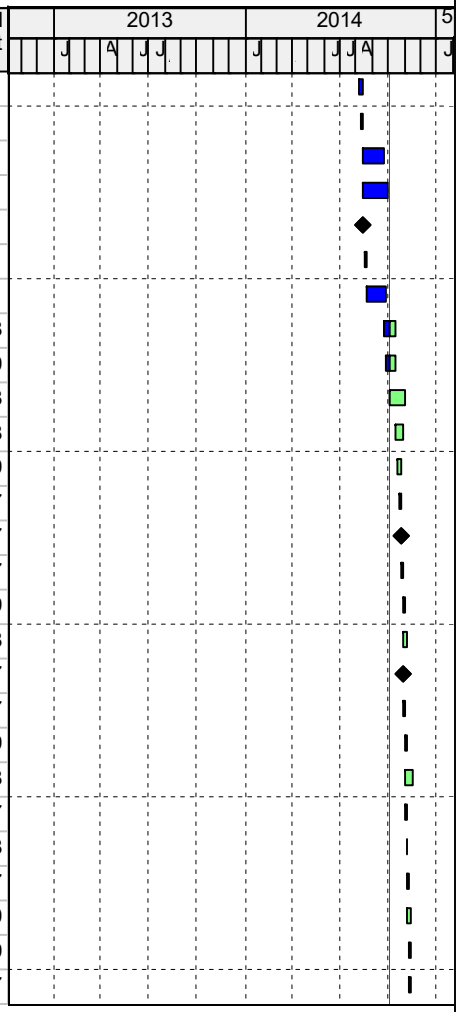


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6014 | Elev 6 - Install Cab/Wiring/Door Operator(s) | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 17 |
| EL-3422 | Elev 3&4 - Adjust | 8 | 8 | 18-Nov-14 | 01-Dec-14 | 18 |
| EL-6022 | Elev 6 - Adjust | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 17 |
| EL-6024 | Elev 6 - Clean / Paint / Punchlist | 1 | 1 | 01-Dec-14 | 01-Dec-14 | 17 |
| EL-3424 | Elev 3&4 - Clean / Paint / Punchlist | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 18 |
| EL-6026 | Elev 6 - Inspections | 1 | 1 | 02-Dec-14 | 02-Dec-14 | 27 |
| EL-3426 | Elev 3&4 - Inspections | 7 | 7 | 09-Dec-14 | 15-Dec-14 | 29 |
| **Exterior Shell** | | | | | | |
| **Elevations** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2** | | | | | | |
| L3D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Feb-14 A | 12-Feb-14 A | |
| L3-5308 | L3- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 17-Feb-14 A | 21-Feb-14 A | |
| L4D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Feb-14 A | 19-Feb-14 A | |
| L4-5308 | L4- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Feb-14 A | 28-Feb-14 A | |
| L5D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Feb-14 A | 26-Feb-14 A | |
| L5-5308 | L5- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 03-Mar-14 A | 07-Mar-14 A | |
| L6D5308 | Deliver/Stock Wall Panels | 1 | 0 | 05-Mar-14 A | 05-Mar-14 A | |
| L6-5308 | L6- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L7-5308 | L7- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L7D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Mar-14 A | 12-Mar-14 A | |
| L8D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Mar-14 A | 19-Mar-14 A | |
| L8-5308 | L8- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Mar-14 A | 28-Mar-14 A | |
| L9D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L9-5308 | L9- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 31-Mar-14 A | 07-Apr-14 A | |
| 10D5308 | Deliver/Stock Wall Panels | 1 | 0 | 02-Apr-14 A | 02-Apr-14 A | |
| L10-5308 | L10- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 07-Apr-14 A | 11-Apr-14 A | |

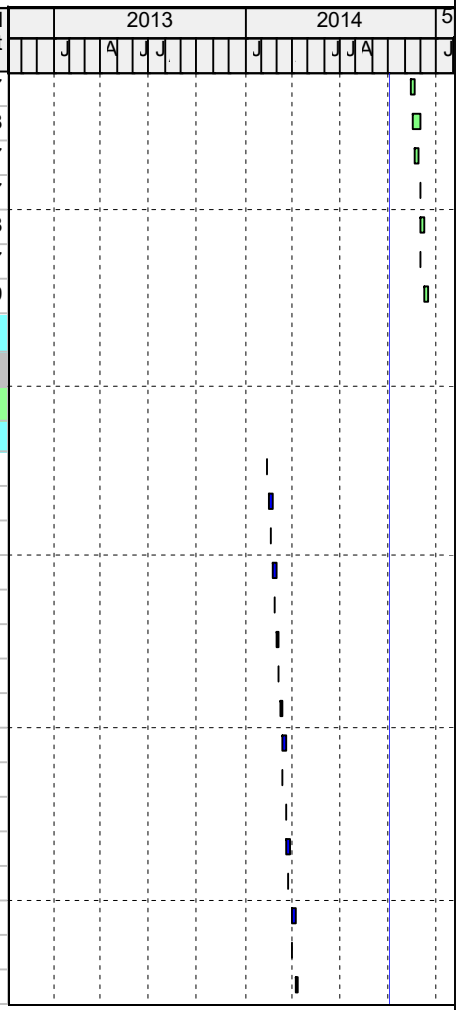



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| 11D5308 | Deliver/Stock Wall Panels | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L11-5308 | L11- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 11-Apr-14 A | 18-Apr-14 A | |
| 12D5308 | Deliver/Stock Wall Panels | 1 | 0 | 16-Apr-14 A | 16-Apr-14 A | |
| L12-5308 | L12- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Apr-14 A | 25-Apr-14 A | |
| 14D5308 | Deliver/Stock Wall Panels | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L14-5308 | L14 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Apr-14 A | 01-May-14 A | |
| 15D5308 | Deliver/Stock Wall Panels | 1 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L15-5308 | L15 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| 16D5308 | Deliver/Stock Wall Panels | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L16-5308 | L16- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| 17D5308 | Deliver/Stock Wall Panels | 1 | 0 | 14-May-14 A | 14-May-14 A | |
| L17-5308 | L17 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 20-May-14 A | 11-Jun-14 A | |
| LL2-5308 | LL2 Thru L4 - Support Frame/Sheathing for Metal Wa | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL1-5308 | LL1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| L1-5308 | L1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| **Level 1** | | | | | | |
| L3-5102 | L3- Storefront Frames | 7 | 0 | 18-Aug-14 A | 29-Sep-14 A | |
| L1-5102 | L1 - Storefront Frames (excl. Main Entry Facade) | 8 | 0 | 02-Sep-14 A | 11-Sep-14 A | |
| L1-5104 | L1 - Storefront Glazing (excl. Main Entry Facade) | 4 | 0 | 19-Sep-14 A | 24-Sep-14 A | |
| EP-5110 | L1 - Revolving Doors | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L3-5104 | L3 - Storefront Glazing | 3 | 0 | 30-Sep-14 A | 03-Oct-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Levels 3-4** | | | | | | |
| L3-5130 | L3 - Install Punch Windows | 5 | 0 | 24-Feb-14 A | 10-Mar-14 A | |
| L4-5130 | L4 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 12-Mar-14 A | |
| L5-5130 | L5 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L6-5130 | L6- Install Punch Windows | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |

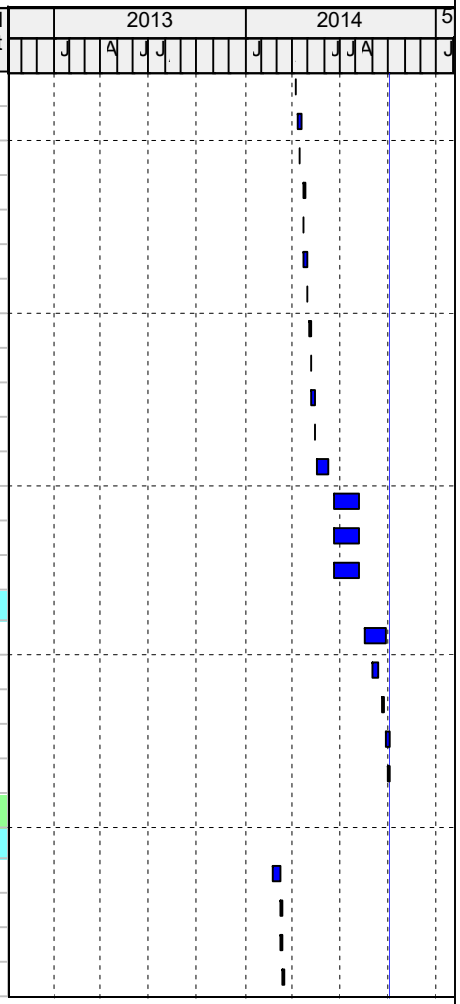



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L7-5130 | L7 - Install Punch Windows | 5 | 0 | 18-Mar-14 A | 21-Mar-14 A | |
| L8-5130 | L8 - Install Punch Windows | 5 | 0 | 24-Mar-14 A | 28-Mar-14 A | |
| L9-5130 | L9 - Install Punch Windows | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L10-5130 | L10 - Install Punch Windows | 5 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-5130 | L11 - Install Punch Windows | 5 | 0 | 14-Apr-14 A | 21-Apr-14 A | |
| L12-5130 | L12 - Install Punch Windows | 5 | 0 | 22-Apr-14 A | 25-Apr-14 A | |
| L14-5130 | L14 - Install Punch Windows | 5 | 0 | 28-Apr-14 A | 05-May-14 A | |
| L15-5130 | L15 - Install Punch Windows | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| L16-5130 | L16 - Install Punch Windows | 5 | 0 | 12-May-14 A | 20-May-14 A | |
| L17-5130 | L17 - Install Punch Windows | 5 | 0 | 27-May-14 A | 16-Jun-14 A | |
| Roofs | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| RF-4026 | L1 - City Park - Protection Board | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| **Pool Membrane - (elev 18')** | | | | | | |
| RF-4034 | Pool - Install plumbing | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 9 |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |
| RF-4010 | AR - Set Mechanical Equipment | 5 | 0 | 10-Jun-14 A | 12-Jun-14 A | |
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 10 | 0 | 04-Aug-14 A | 27-Aug-14 A | |
| RF-4012 | L2.5 Horseshoe - Install corrugated metal panels | 4 | 4 | 22-Oct-14 | 27-Oct-14 | 40 |
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 8 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |
| PC-4008 | RF - Entry / Porte Cochere Roofing System | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | RF - Upper Ballroom Roofing System | 3 | 0 | 28-Jul-14 A | 31-Jul-14 A | |

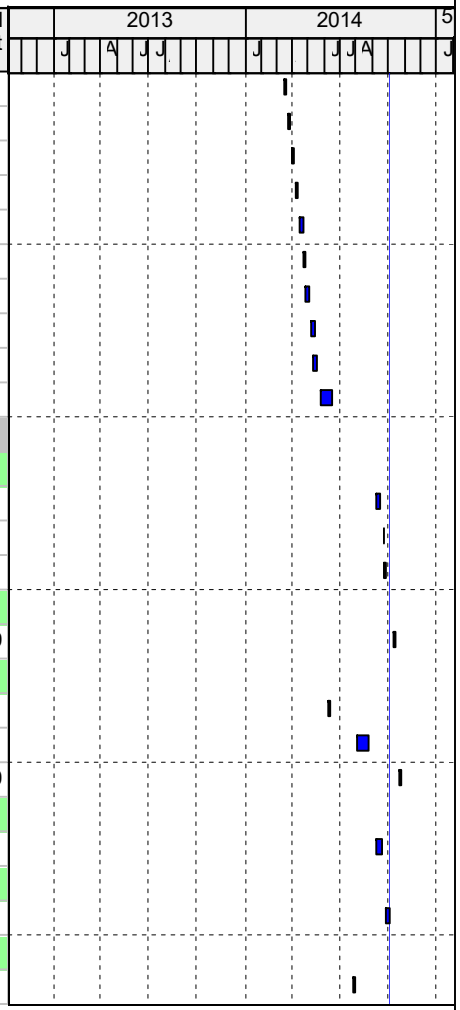



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 4 | 0 | 31-Jul-14 A | 04-Aug-14 A | |
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |
| RF-4018 | TR - Terrace Roof - Green Roofing System | 5 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| RF-4020 | TR - Terrace Roof - Install sheet metal capping | 1 | 1 | 04-Nov-14 | 04-Nov-14 | 33 |
| RF-4022 | TR - Terrace Roof - Install deocrative metal railing | 3 | 3 | 05-Nov-14 | 10-Nov-14 | 33 |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Perimeter Framing / Sul | 10 | 0 | 02-Jun-14 A | 08-Jul-14 A | |
| RF-4002 | Tower Roof - Roofing System | 10 | 0 | 20-Aug-14 A | 17-Sep-14 A | |
| **PH - Roof - (elev 173')** | | | | | | |
| RF-4030 | PH - Roofing System | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| RF-4032 | PH - Coping / Flashing [DELETED] | 3 | 0 | 01-Sep-14 A | 01-Sep-14 A | |
| **Rough-In's** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6002 | LL4 - Layout | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| LL4-6008 | LL4 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL4-6012 | LL4 - Fire Sprinkler Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6014 | LL4 - Plumbing Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6018 | LL4 - HVAC Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6004 | LL4 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL4-6016 | LL4 - Electrical Rl | 10 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties Rl | 8 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6010 | LL4 - Elevator pits | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| LL4-6020 | LL4 - H Mtl Frames | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL4-6024 | LL4 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |

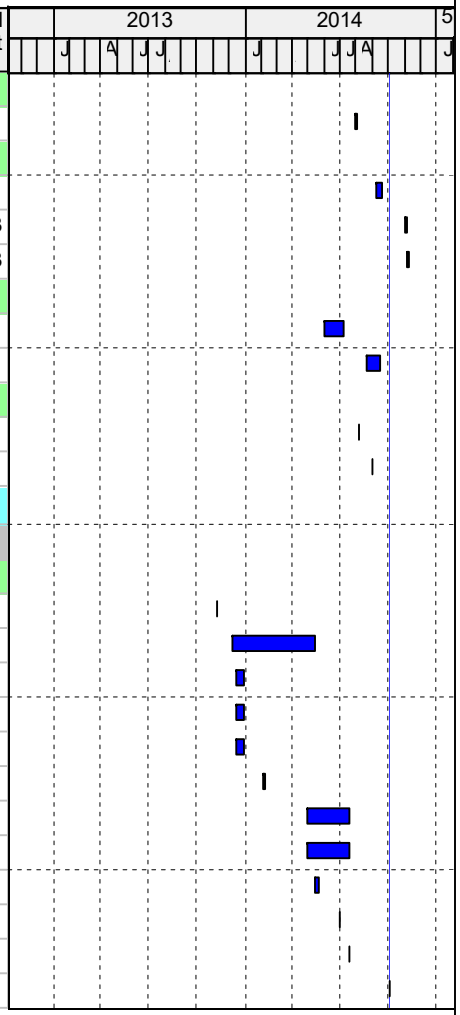



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6002 | LL3 - Layout | 1 | 0 | 19-Nov-13 A | 19-Nov-13 A | |
| LL3-6008 | LL3 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL3-6012 | LL3 - Fire Sprinkler RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6014 | LL3 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6018 | LL3 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6004 | LL3 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL3-6020 | LL3 - H Mtl Frames | 3 | 0 | 08-May-14 A | 09-May-14 A | |
| LL3-6010 | LL3 - F/P Curbs | 5 | 0 | 19-May-14 A | 19-May-14 A | |
| LL3-6016 | LL3 - Electrical RI | 2 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties RI | 8 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL3-6024 | LL3 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6002 | LL2 - Layout | 1 | 0 | 14-Jan-14 A | 14-Jan-14 A | |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| LL2-6012 | LL2 - Fire Sprinkler RI | 10 | 0 | 21-Jan-14 A | 03-Feb-14 A | |
| LL2-6014 | LL2 - Plumbing RI | 10 | 0 | 21-Jan-14 A | 14-Feb-14 A | |
| LL2E-6016 | LL2 - Electrical RI | 8 | 0 | 03-Feb-14 A | 17-Mar-14 A | |
| LL2-6016 | LL2 - Electrical RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2-6018 | LL2 - HVAC RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2–6004 | LL2 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL2E-6004 | LL2 - CMU Walls | 10 | 0 | 04-Mar-14 A | 09-May-14 A | |
| LL2E-6012 | LL2 - Fire Sprinkler RI | 8 | 0 | 21-Mar-14 A | 01-Apr-14 A | |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 24-Apr-14 A | |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 3 | 0 | 23-Apr-14 A | 21-Jul-14 A | |
| LL2E-6020 | LL2 - H Mtl Frames | 3 | 0 | 09-May-14 A | 12-May-14 A | |

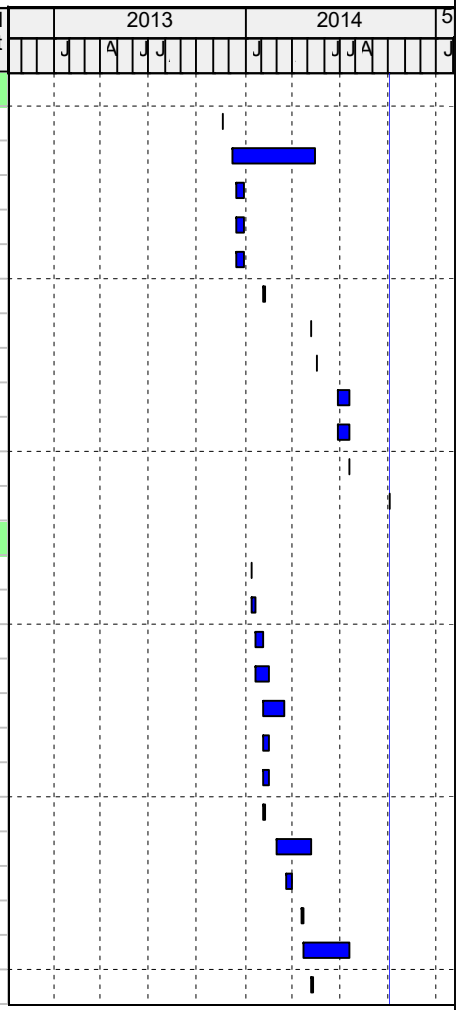



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-6020 | LL2 - H Mtl Frames | 3 | 0 | 12-May-14 A | 13-May-14 A | |
| LL2E-6008 | LL2 - Int Wall Framing | 5 | 0 | 13-May-14 A | 22-Jun-14 A | |
| LL2E-6014 | LL2 - Plumbing RI | 8 | 0 | 13-May-14 A | 30-May-14 A | |
| LL2E-6018 | LL2 - HVAC RI | 8 | 0 | 13-May-14 A | 04-Aug-14 A | |
| LL2E-6022 | LL2 - Fire Alarm / Elec Specialties RI (East of 10) | 8 | 0 | 13-May-14 A | 22-Sep-14 A | |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties RI (West of 10) | 8 | 0 | 19-May-14 A | 22-Sep-14 A | |
| LL2-6015 | LL2 - Main Elect Room Set Equip / RI - Power to Ma | 15 | 0 | 30-Jun-14 A | 26-Sep-14 A | |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 0 | 16-Jul-14 A | 21-Jul-14 A | |
| LL2-6024 | LL2 - Inspections | 2 | 0 | 15-Sep-14 A | 03-Oct-14 A | |
| LL2-6010 | LL2 - F/P Curbs @ Parking | 4 | 4 | 09-Oct-14 | 14-Oct-14 | 51 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6002 | Layout | 3 | 0 | 03-Jan-14 A | 08-Jan-14 A | |
| LL1-6008 | Int Wall Framing & Inspection | 6 | 0 | 08-Jan-14 A | 21-Jul-14 A | |
| LL1-Z2-6002 | Layout | 3 | 0 | 08-Jan-14 A | 14-Jan-14 A | |
| LL1-Z3-6002 | Layout | 3 | 0 | 14-Jan-14 A | 17-Jan-14 A | |
| LL1-Z2-6008 | Int Wall Framing & Inspection | 6 | 0 | 17-Jan-14 A | 01-Aug-14 A | |
| LL1-Z3-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-Jan-14 A | 04-Aug-14 A | |
| LL1-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 09-May-14 A | |
| LL1-Z2-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 28-Apr-14 A | |
| LL1-Z3-6004 | CMU Walls (At All Areas North of Q-Line) | 3 | 0 | 03-Feb-14 A | 13-May-14 A | |
| LL1C-6012 | Complete Fire Sprinkler RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6016 | Complete Electrical RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 10 | 0 | 17-Feb-14 A | 16-Sep-14 A | |
| LL1C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 30-Apr-14 A | |

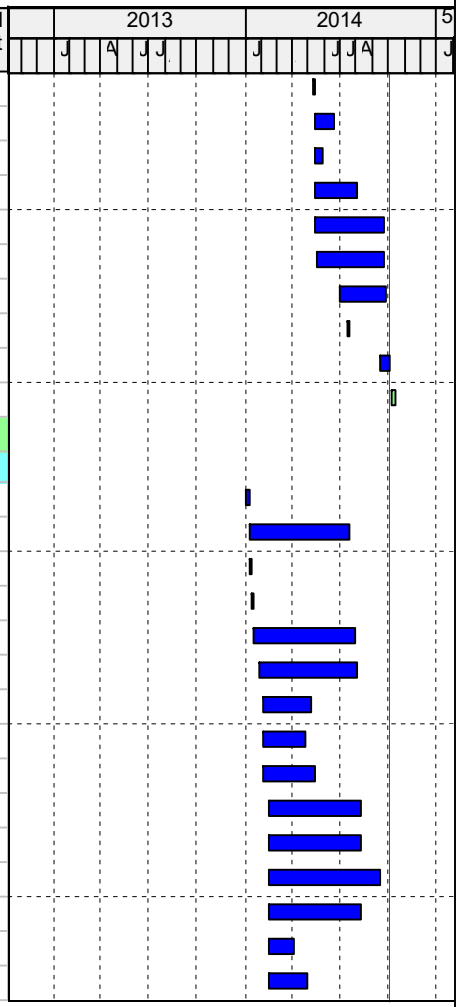



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-Z2-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z2-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z3-6012 | Fire Sprinkler RI (At All Areas North of Q-Line) | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z3-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 11-Sep-14 A | |
| LL1-Z3-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z2C-6012 | Complete Fire Sprinkler RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6014 | Complete Plumbing RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6016 | Complete Electrical RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 15 | 0 | 24-Feb-14 A | 15-Sep-14 A | |
| LL1-Z2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2-6020 | Hollow Metal Door Frames | 5 | 0 | 17-Mar-14 A | 04-Apr-14 A | |
| LL1-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| LL1-Z3-6020 | Hollow Metal Door Frames (At All Areas North of Q-Lir | 1 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| L1B-6004 | CMU Walls [including East Service Corridor] | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L1L-6002 | Layout [including back of house] | 3 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 29-Apr-14 A | |
| L1B-6008 | Int Wall Framing & Inspection | 6 | 0 | 21-Apr-14 A | 08-Aug-14 A | |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 5 | 0 | 25-Apr-14 A | 21-Jul-14 A | |
| LL1C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 30-Apr-14 A | 30-Apr-14 A | |

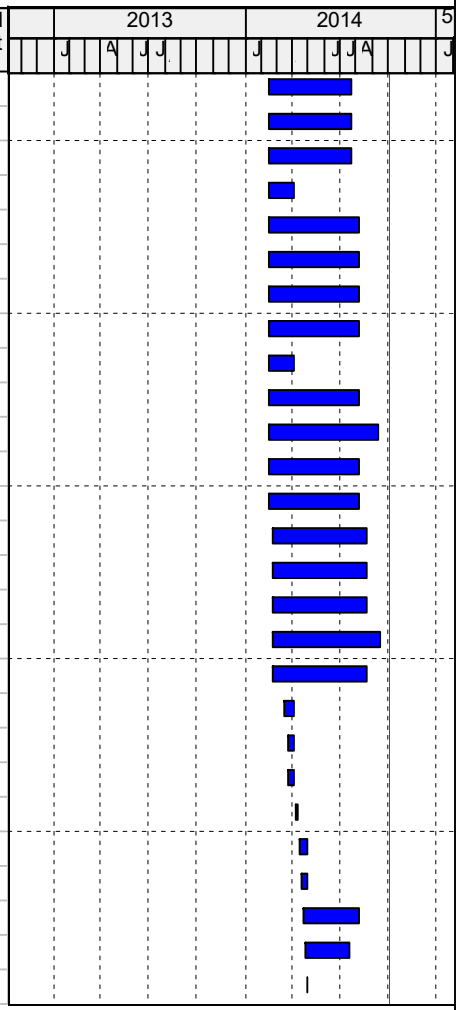


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-6004 | CMU Walls [including public restroom] | 3 | 0 | 05-May-14 A | 08-May-14 A | |
| L1K-6002 | Layout [including public restroom] | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| L1K-6008 | Int Wall Framing & Inspection | 4 | 0 | 09-May-14 A | 22-Aug-14 A | |
| L1B-6002 | Layout [including East Service Corridor] | 3 | 0 | 14-May-14 A | 27-May-14 A | |
| L1L-6008 | Int Wall Framing & Inspection | 6 | 1 | 27-May-14 A | 06-Oct-14 | 0 |
| L1L-6004 | CMU Walls [including back of house] | 3 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L1K-6012 | Fire Sprinkler RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6014 | Plumbing RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6016 | Electrical RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1K-6018 | HVAC RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1B-6014 | Plumbing RI [including East Service Corridor] | 10 | 0 | 16-Jun-14 A | 24-Jun-14 A | |
| L1B-6018 | HVAC RI | 10 | 0 | 20-Jun-14 A | 15-Aug-14 A | |
| L1B-6012 | Fire Sprinkler RI | 10 | 0 | 21-Jun-14 A | 15-Aug-14 A | |
| L1L-6018 | HVAC RI | 5 | 2 | 23-Jun-14 A | 08-Oct-14 | 0 |
| L1L-6014 | Plumbing RI | 5 | 2 | 24-Jun-14 A | 08-Oct-14 | 0 |
| L1L-6010 | CMU Seismic Clips [including back of house] [DELET | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1L-6012 | Fire Sprinkler RI | 5 | 2 | 25-Jun-14 A | 08-Oct-14 | 0 |
| L1L-6016 | Electrical RI | 5 | 2 | 25-Jun-14 A | 08-Oct-14 | 0 |
| L1L-6022 | Fire Alarm / Elec Specialties RI | 5 | 2 | 27-Jun-14 A | 08-Oct-14 | 0 |
| L1K-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 27-Jun-14 A | 29-Sep-14 A | |
| LL1-Z3-6009 | Frame Ceilings [DELETED] | 4 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1B-6016 | Electrical RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| L1B-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| LL1-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-Z2-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L1B-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-6024 | Inspections for Cover | 1 | 0 | 23-Jul-14 A | 24-Jul-14 A | |

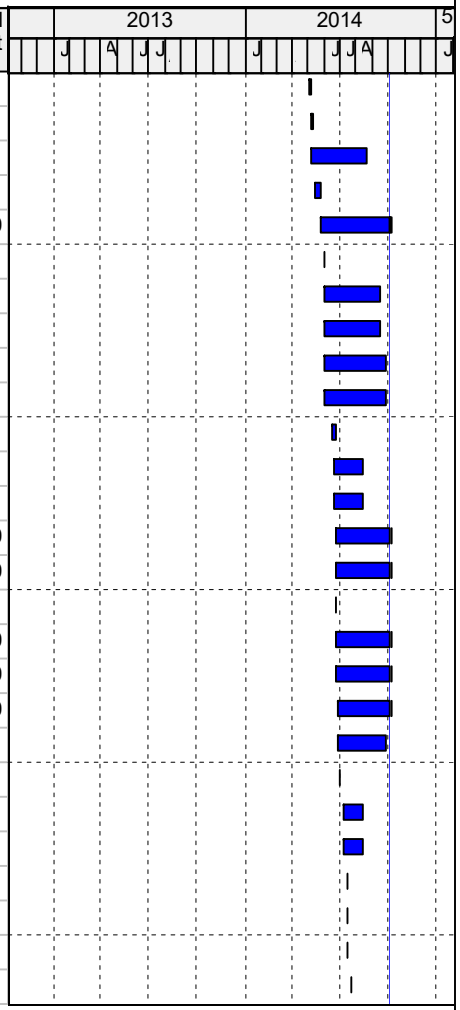


Actual Work | Remaining Work | Critical Remai... | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-6020 | Hollow Metal Door Frames | 5 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| LL1-Z3-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L1K-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 06-Aug-14 A | |
| LL1-Z2-6024 | Inspections for Cover | 2 | 0 | 07-Aug-14 A | 08-Aug-14 A | |
| L1K-6020 | Hollow Metal Door Frames | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-Z2-6009 | Frame Ceilings & Inspection | 6 | 3 | 22-Aug-14 A | 08-Oct-14 | 19 |
| L1L-6020 | Hollow Metal Door Frames | 5 | 1 | 25-Aug-14 A | 06-Oct-14 | 2 |
| LL1-6009 | Frame Ceilings & Inspection (except for bar redesign | 9 | 1 | 02-Sep-14 A | 06-Oct-14 | 32 |
| LL1-Z3-6024 | Inspections for Cover | 2 | 0 | 12-Sep-14 A | 12-Sep-14 A | |
| LL1-Z3C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6016 | Complete Electrical RI @ Ceilings | 5 | 1 | 15-Sep-14 A | 08-Oct-14 | 26 |
| LL1-Z3C-6018 | Complete HVAC RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 1 | 15-Sep-14 A | 08-Oct-14 | 26 |
| L1KC-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 4 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L1B-6024 | Inspections for Cover (Main Ballroom N/S/W Walls & | 3 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1K-6024 | Inspections for Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1K-6009 | Frame Ceilings [public restroom] | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 20 |
| L1KC-6014 | Complete Plumbing RI @ Ceilings & Inspection | 4 | 4 | 07-Oct-14 | 10-Oct-14 | 20 |
| L1KC-6016 | Complete Electrical RI @ Ceilings & Inspection | 4 | 4 | 07-Oct-14 | 10-Oct-14 | 20 |
| L1KC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 4 | 4 | 07-Oct-14 | 10-Oct-14 | 20 |
| L1KC-6018 | Complete HVAC RI @ Ceilings & Inspection | 4 | 4 | 08-Oct-14 | 13-Oct-14 | 19 |
| L1L-6024 | Inspections for Cover | 2 | 2 | 09-Oct-14 | 10-Oct-14 | 0 |
| L1BC-6012 | Complete Fire Sprinkler RI @ Ceilings | 7 | 7 | 17-Oct-14 | 27-Oct-14 | 1 |
| L1BC-6014 | Complete Plumbing RI @ Ceilings | 7 | 7 | 17-Oct-14 | 27-Oct-14 | 1 |
| L1BC-6018 | Complete HVAC RI @ Ceilings | 7 | 7 | 17-Oct-14 | 27-Oct-14 | 1 |
| L1B-6009 | Frame Ceilings | 7 | 7 | 27-Oct-14 | 04-Nov-14 | 1 |

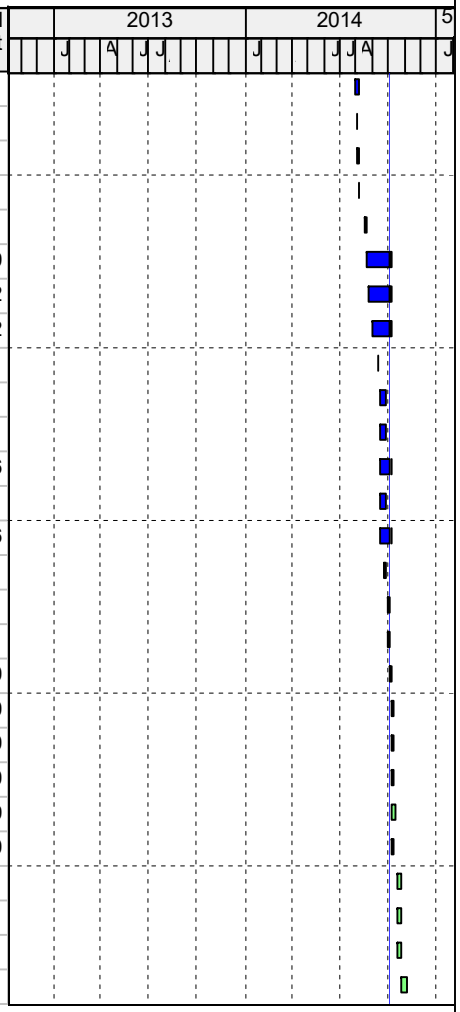



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-6009 | Frame Ceilings & Inspection | 13 | 13 | 29-Oct-14 | 14-Nov-14 | 0 |
| L1LC-6012 | Complete Fire Sprinkler RI @ Ceilings | 4 | 4 | 29-Oct-14 | 03-Nov-14 | 0 |
| L1LC-6014 | Complete Plumbing RI @ Ceilings | 4 | 4 | 29-Oct-14 | 03-Nov-14 | 0 |
| L1LC-6016 | Complete Electrical RI @ Ceilings | 4 | 4 | 29-Oct-14 | 03-Nov-14 | 0 |
| L1LC-6018 | Complete HVAC RI @ Ceilings | 4 | 4 | 29-Oct-14 | 03-Nov-14 | 0 |
| L1LC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 4 | 4 | 29-Oct-14 | 03-Nov-14 | 0 |
| L1BC-6016 | Complete Electrical RI @ Ceilings & Inspection | 7 | 7 | 30-Oct-14 | 07-Nov-14 | 1 |
| L1BC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 7 | 7 | 30-Oct-14 | 07-Nov-14 | 1 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 0 | 17-Apr-14 A | 09-May-14 A | |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6006 | L2 - Support Frame/Sheathing for Metal Panels | 6 | 0 | 23-Apr-14 A | 07-Aug-14 A | |
| L02-6008 | L2 - Int Wall Framing | 10 | 0 | 25-Apr-14 A | 17-Jul-14 A | |
| L02-6014 | L2 - Plumbing RI | 15 | 0 | 28-Apr-14 A | 07-Aug-14 A | |
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 0 | 28-Apr-14 A | 09-May-14 A | |
| L02-6004 | L2 - CMU Walls | 5 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L02-6002 | L2 - Layout | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L02-6018 | L2 - HVAC RI (including equipment) | 20 | 0 | 18-Jun-14 A | 10-Sep-14 A | |
| L02-6016 | L2 - Electrical RI | 10 | 0 | 24-Jun-14 A | 14-Aug-14 A | |
| L02-6022 | L2 - Fire Alarm / Elec Specialties RI | 10 | 1 | 24-Jun-14 A | 06-Oct-14 | 29 |
| L02-6012 | L2 - Fire Sprinkler RI | 10 | 0 | 26-Jun-14 A | 07-Aug-14 A | |
| L02-6020 | L2 - H Mtl Frames | 5 | 0 | 11-Jul-14 A | 17-Jul-14 A | |
| L02-6024 | L2 - Inspections - North Half | 2 | 2 | 10-Oct-14 | 13-Oct-14 | 25 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L07-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 01-Apr-11 A | 11-Apr-11 A | |

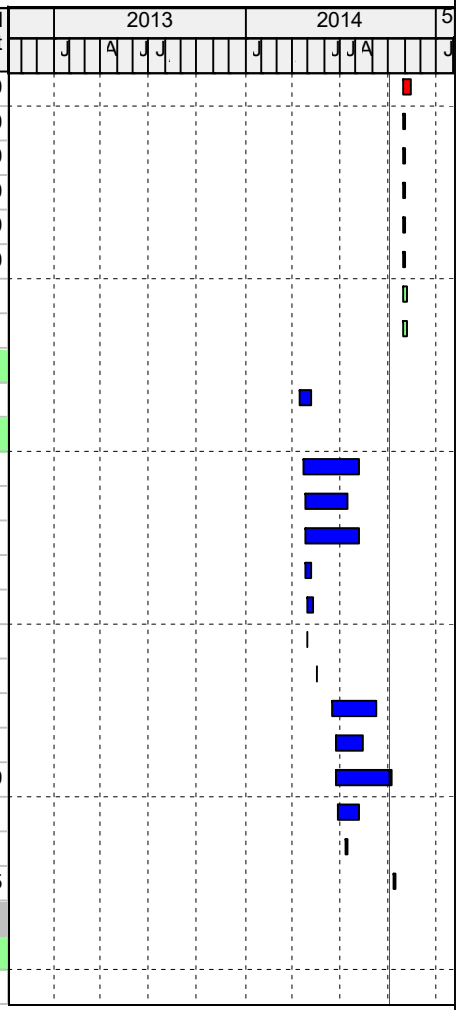



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6012 | Fire Sprinkler Mains | 5 | 0 | 01-Feb-14 A | 03-Apr-14 A | |
| L03-8219 | HVAC Risers | 5 | 0 | 11-Feb-14 A | 23-Mar-14 A | |
| L03-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 11-Feb-14 A | 03-Mar-14 A | |
| L03-6002 | Layout | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| L04-8219 | HVAC Risers | 5 | 0 | 13-Feb-14 A | 23-Mar-14 A | |
| L05-8219 | HVAC Risers | 5 | 0 | 17-Feb-14 A | 03-Mar-14 A | |
| L03-6008 | Frame Shaft Walls | 3 | 0 | 18-Feb-14 A | 26-Mar-14 A | |
| L04-6002 | Layout | 5 | 0 | 19-Feb-14 A | 25-Feb-14 A | |
| L04-6008 | Frame Shaft Walls | 3 | 0 | 20-Feb-14 A | 26-Mar-14 A | |
| L03-6011 | PreRock Shafts | 2 | 0 | 24-Feb-14 A | 25-Mar-14 A | |
| L03-6010 | Frame Walls | 5 | 0 | 25-Feb-14 A | 25-Mar-14 A | |
| L05-6002 | Layout | 5 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| L04-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 28-Feb-14 A | 05-Mar-14 A | |
| L03-6016 | Electrical RI | 5 | 0 | 03-Mar-14 A | 04-Apr-14 A | |
| L03-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 12-Mar-14 A | |
| L04-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 13-Mar-14 A | |
| L04-6010 | Frame Walls | 5 | 0 | 04-Mar-14 A | 05-Jun-14 A | |
| L05-6008 | Frame Shaft Walls | 3 | 0 | 05-Mar-14 A | 27-Mar-14 A | |
| L06-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L07-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L05-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 06-Mar-14 A | 21-Mar-14 A | |
| L03-6020 | Install Hollow Metal Frames | 3 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L04-6020 | Install Hollow Metal Frames | 3 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L05-6010 | Frame Walls | 5 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L06-6002 | Layout | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L04-6011 | PreRock Shafts | 2 | 0 | 18-Mar-14 A | 25-Mar-14 A | |
| L05-6009 | Inspect Shafts | 1 | 0 | 18-Mar-14 A | 18-Mar-14 A | |

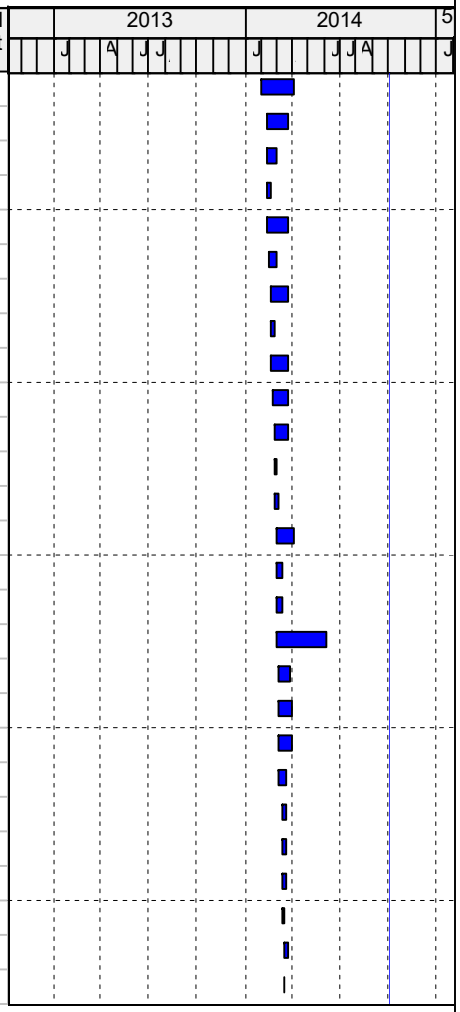



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| L06-6008 | Frame Shaft Walls | 3 | 0 | 19-Mar-14 A | 03-Apr-14 A | |
| L06-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 27-Mar-14 A | |
| L04-6016 | Electrical RI | 5 | 0 | 20-Mar-14 A | 09-Apr-14 A | |
| L05-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 26-Mar-14 A | |
| L06-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 07-Apr-14 A | |
| L07-6002 | Layout | 5 | 0 | 24-Mar-14 A | 30-Apr-14 A | |
| L03-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L03-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L05-6016 | Electrical RI | 5 | 0 | 25-Mar-14 A | 05-Jun-14 A | |
| L04-6019 | Complete Top Out GWB | 2 | 0 | 26-Mar-14 A | 06-Jun-14 A | |
| L05-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L06-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| L03-6019 | Complete Top Out GWB | 2 | 0 | 27-Mar-14 A | 02-May-14 A | |
| L08-6002 | Layout | 5 | 0 | 27-Mar-14 A | 02-Apr-14 A | |
| L05-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 28-Mar-14 A | 03-Apr-14 A | |
| L06-6010 | Frame Walls | 5 | 0 | 28-Mar-14 A | 07-Apr-14 A | |
| L03-6012 | Fire Sprinkler Mains | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L07-6008 | Frame Shaft Walls | 3 | 0 | 31-Mar-14 A | 03-Apr-14 A | |
| L05-6019 | Complete Top Out GWB | 2 | 0 | 01-Apr-14 A | 08-Apr-14 A | |
| L08-6008 | Frame Shaft Walls | 3 | 0 | 02-Apr-14 A | 21-Apr-14 A | |
| L03-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L04-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L05-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L06-6016 | Electrical RI | 5 | 0 | 03-Apr-14 A | 15-Apr-14 A | |

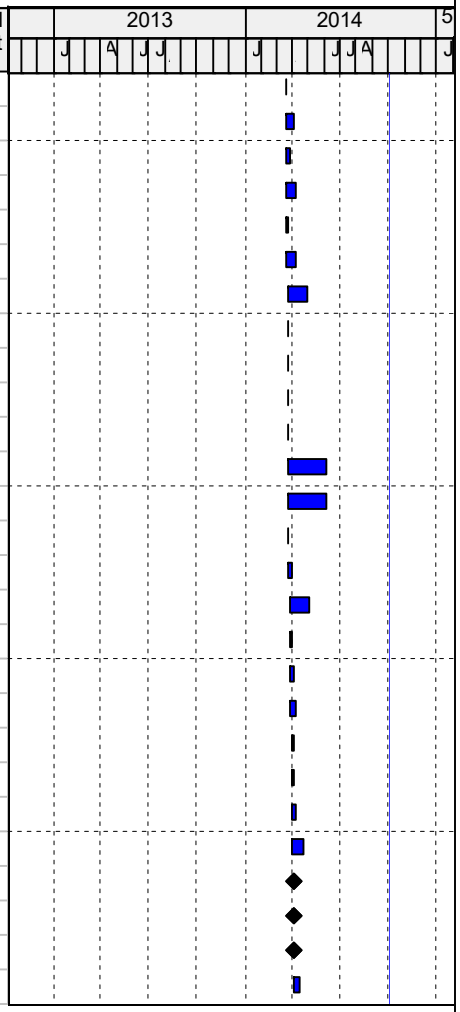



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6009 | Inspect Shafts | 1 | 0 | 03-Apr-14 A | 03-Apr-14 A | |
| L07-6011 | PreRock Shafts | 2 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| L05-6012 | Fire Sprinkler Mains | 5 | 0 | 04-Apr-14 A | 30-Apr-14 A | |
| L06-6012 | Fire Sprinkler Mains | 5 | 0 | 07-Apr-14 A | 30-Apr-14 A | |
| L06-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L06-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L07-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| L07-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L03-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L03-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L04-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L06-6009 | Inspect Shafts | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L06-6019 | Complete Top Out GWB | 2 | 0 | 08-Apr-14 A | 18-Apr-14 A | |
| L07-6010 | Frame Walls | 5 | 0 | 08-Apr-14 A | 15-Apr-14 A | |
| L08-6011 | PreRock Shafts | 2 | 0 | 08-Apr-14 A | 23-Apr-14 A | |
| L09-6002 | Layout | 5 | 0 | 08-Apr-14 A | 26-Apr-14 A | |
| L03-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 09-Apr-14 A | 08-May-14 A | |
| L03-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L05-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 09-Apr-14 A | 14-Apr-14 A | |
| L08-6009 | Inspect Shafts | 1 | 0 | 09-Apr-14 A | 25-Apr-14 A | |
| L09-6008 | Frame Shaft Walls | 3 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| L08-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| L04-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 15-Apr-14 A | 16-Apr-14 A | |
| L07-6012 | Fire Sprinkler Mains | 5 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| L07-6016 | Electrical RI | 5 | 0 | 15-Apr-14 A | 12-May-14 A | |
| L07-6020 | Install Hollow Metal Frames | 3 | 0 | 16-Apr-14 A | 23-Apr-14 A | |
| L05-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 17-Apr-14 A | 25-Apr-14 A | |

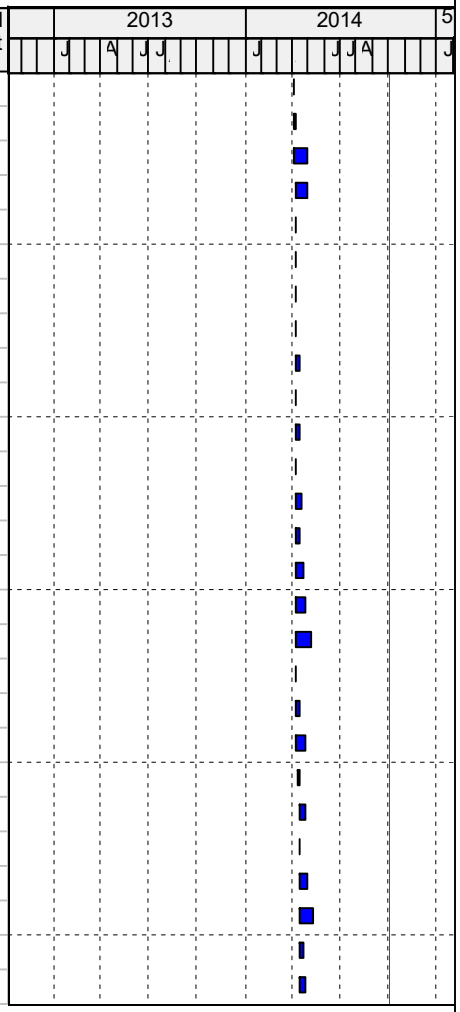



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 17-Apr-14 A | 12-May-14 A | |
| L06-6023 | Inspection of Exterior Framing | 0 | 0 | 17-Apr-14 A | | |
| L09-8219 | HVAC Risers | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L09-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L04-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 18-Apr-14 A | 20-Apr-14 A | |
| L04-6028 | PreRock at Heat Pumps | 2 | 0 | 20-Apr-14 A | 22-Apr-14 A | |
| L08-8219 | HVAC Risers | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6009 | Inspect Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6011 | PreRock Shafts | 2 | 0 | 22-Apr-14 A | 24-Apr-14 A | |
| L04-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L06-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 23-Apr-14 A | 25-Apr-14 A | |
| L08-6020 | Install Hollow Metal Frames | 3 | 0 | 23-Apr-14 A | 13-May-14 A | |
| L11-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L11-8220 | Plumbing Risers - Install | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L04-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L09-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L10-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L10-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 20-May-14 A | |
| L12-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L04-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 25-Apr-14 A | 11-Jun-14 A | |
| L04-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L09-6010 | Frame Walls | 5 | 0 | 25-Apr-14 A | 20-May-14 A | |
| L09-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L10-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L11-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 30-Apr-14 A | |

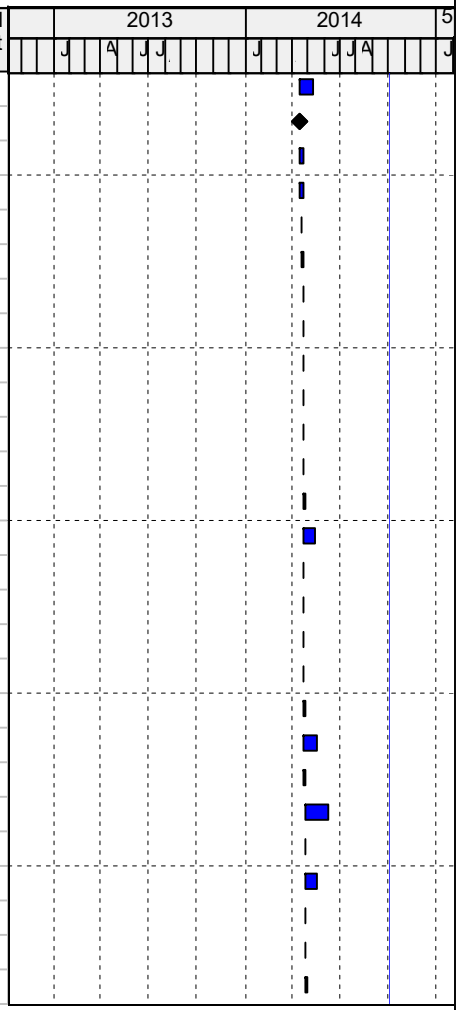



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L08-6010 | Frame Walls | 5 | 0 | 26-Apr-14 A | 30-Apr-14 A | |
| L10-6002 | Layout | 5 | 0 | 27-Apr-14 A | 27-Apr-14 A | |
| L04-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 28-Apr-14 A | 30-Apr-14 A | |
| L05-6018 | HVAC RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6028 | PreRock at Heat Pumps | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L07-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 28-Apr-14 A | 12-May-14 A | |
| L10-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-Apr-14 A | 22-May-14 A | |
| L11-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L12-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L05-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| L05-6028 | PreRock at Heat Pumps | 2 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L06-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 09-May-14 A | |
| L06-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L06-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L08-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L08-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L09-6020 | Install Hollow Metal Frames | 3 | 0 | 29-Apr-14 A | 20-May-14 A | |
| L09-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |

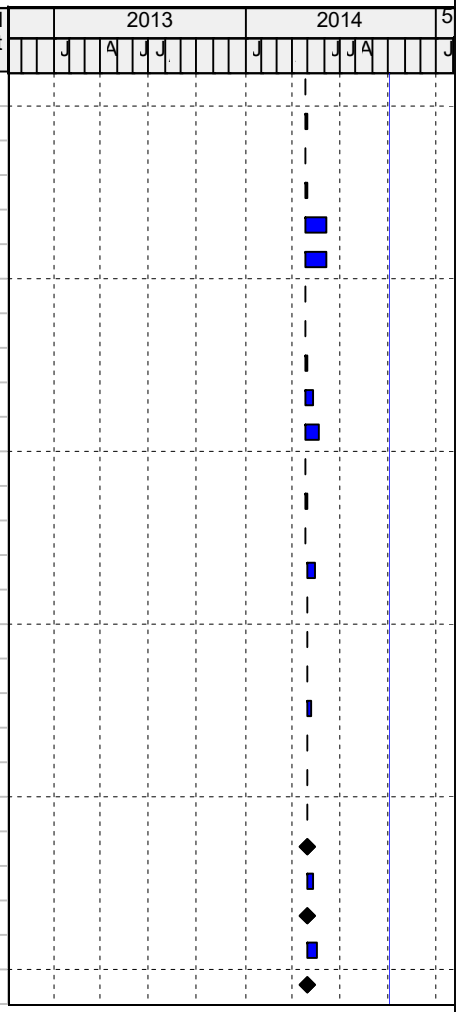



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L04-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 30-Apr-14 A | 02-May-14 A | |
| L09-6019 | Complete Top Out GWB | 2 | 0 | 30-Apr-14 A | 06-Jun-14 A | |
| L11-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L12-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L03-6028 | PreRock at Heat Pumps | 2 | 0 | 01-May-14 A | 02-May-14 A | |
| L05-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L06-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L03-6014 | Set Tubs & Plumbing RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L05-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L05-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| L06-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L06-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 09-May-14 A | |
| L03-6018 | HVAC RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L03-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 06-May-14 A | 06-May-14 A | |
| L07-6014 | Set Tubs & Plumbing RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L07-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 06-May-14 A | 09-May-14 A | |
| L03-6004 | CMU Wall/Clips | 3 | 0 | 07-May-14 A | 08-May-14 A | |
| L03-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L03-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 08-May-14 A | 13-May-14 A | |
| L03-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6004 | CMU Walls | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6018 | HVAC RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |

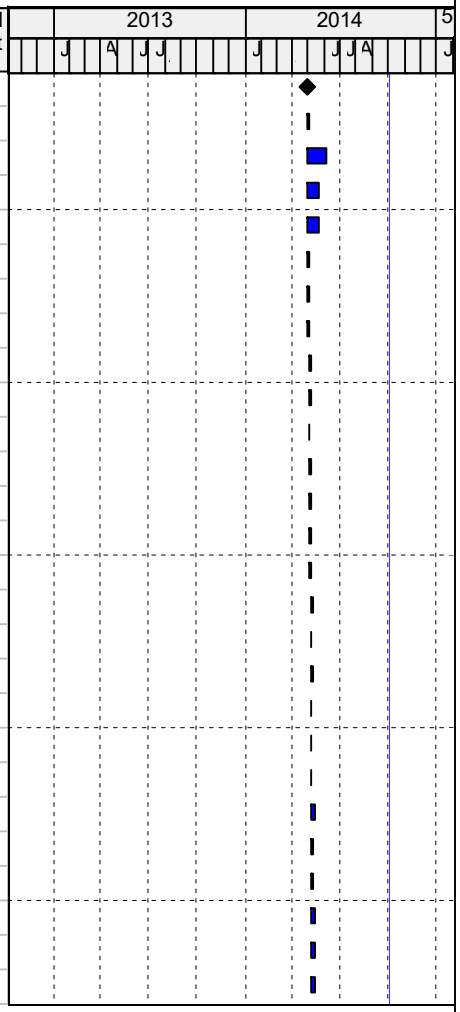



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L11-6010 | Frame Walls | 5 | 0 | 09-May-14 A | 15-May-14 A | |
| L05-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 12-May-14 A | 05-Jun-14 A | |
| L07-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 12-May-14 A | 13-May-14 A | |
| L11-6020 | Install Hollow Metal Frames | 3 | 0 | 12-May-14 A | 14-May-14 A | |
| L11-6019 | Complete Top Out GWB | 2 | 0 | 12-May-14 A | 14-May-14 A | |
| L14-6002 | Layout | 5 | 0 | 12-May-14 A | 14-May-14 A | |
| L15-6002 | Layout | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L05-6004 | CMU Walls | 3 | 0 | 13-May-14 A | 13-May-14 A | |
| L06-6018 | HVAC Rl | 5 | 0 | 13-May-14 A | 25-Jun-14 A | |
| L06-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 13-May-14 A | 14-Jul-14 A | |
| L07-6018 | HVAC Rl | 5 | 0 | 13-May-14 A | 05-Jun-14 A | |
| L07-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| L07-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 13-May-14 A | 13-May-14 A | |
| L14-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L16-6002 | Layout | 5 | 0 | 13-May-14 A | 16-May-14 A | |
| L06-6004 | CMU Walls | 3 | 0 | 14-May-14 A | 14-May-14 A | |
| L07-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 15-May-14 A | |
| L08-6012 | Fire Sprinkler Mains | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6002 | Layout | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L07-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 16-May-14 A | 25-Jun-14 A | |
| L08-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-May-14 A | 16-May-14 A | |

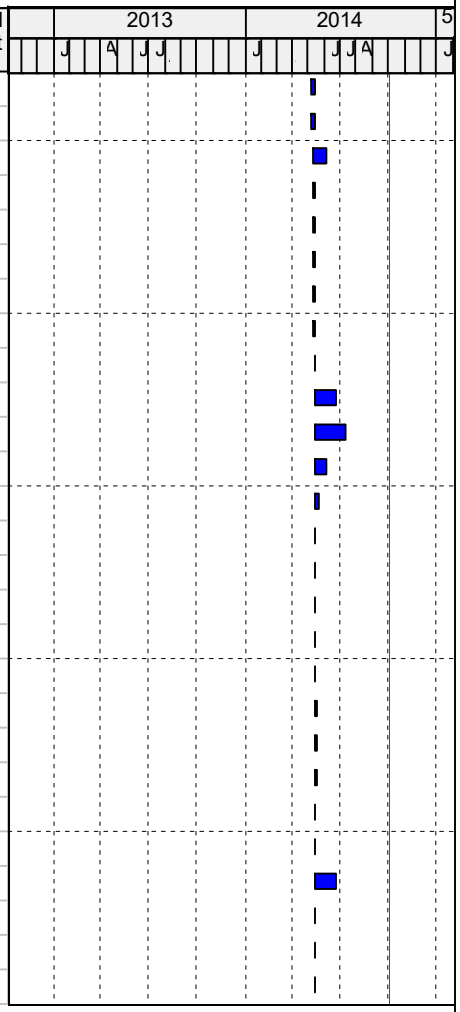


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L12-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L07-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L08-6028 | PreRock at Heat Pumps | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L09-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L10-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L11-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L15-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 19-May-14 A | 19-May-14 A | |
| L07-6028 | PreRock at Heat Pumps | 2 | 0 | 20-May-14 A | 21-May-14 A | |
| L07-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L08-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 20-May-14 A | 21-May-14 A | |
| L10-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L11-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L14-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L07-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 21-May-14 A | 27-May-14 A | |
| L08-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L08-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L09-6028 | PreRock at Heat Pumps | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L10-6014 | Set Tubs & Plumbing RI | 5 | 0 | 21-May-14 A | 27-Jun-14 A | |
| L10-6010 | Frame Walls | 5 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6019 | Complete Top Out GWB | 2 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L11-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L12-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L14-8220 | Plumbing Risers - Install | 2 | 0 | 21-May-14 A | 22-May-14 A | |

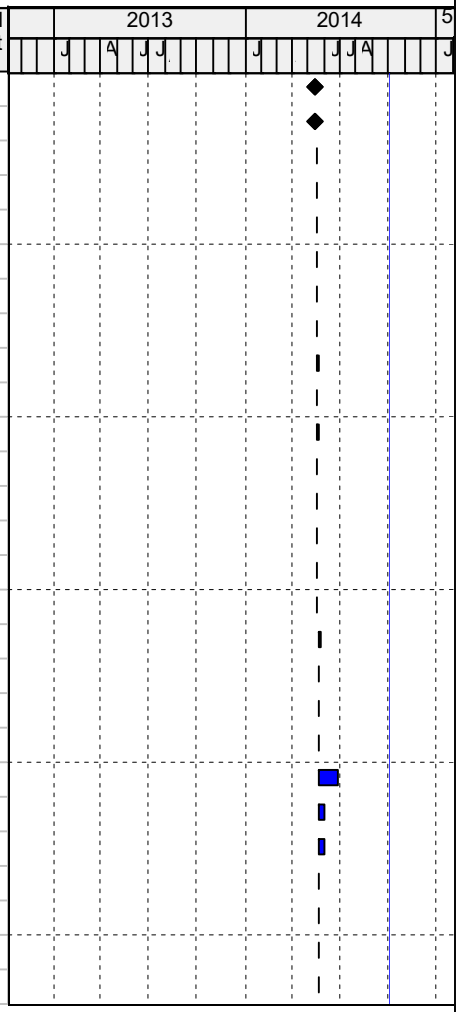



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L16-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L07-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| L08-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 22-May-14 A | 22-May-14 A | |
| L10-6012 | Fire Sprinkler Mains | 5 | 0 | 22-May-14 A | 27-May-14 A | |
| L08-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L09-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6020 | Install Hollow Metal Frames | 3 | 0 | 23-May-14 A | 03-Jun-14 A | |
| L10-6028 | PreRock at Heat Pumps | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L14-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L15-8220 | Plumbing Risers - Install | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L09-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 27-May-14 A | 27-May-14 A | |
| L12-6010 | Frame Walls | 5 | 0 | 27-May-14 A | 02-Jun-14 A | |
| L08-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L09-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 28-May-14 A | 28-May-14 A | |
| L10-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 28-May-14 A | 03-Jun-14 A | |
| L14-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L15-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-May-14 A | 30-May-14 A | |
| L16-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 28-May-14 A | 28-May-14 A | |
| L16-8220 | Plumbing Risers - Install | 2 | 0 | 28-May-14 A | 29-May-14 A | |
| L08-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 29-May-14 A | 30-May-14 A | |
| L10-6016 | Electrical RI | 5 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L10-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| L12-6012 | Fire Sprinkler Mains | 5 | 0 | 30-May-14 A | 26-Jun-14 A | |
| L12-6020 | Install Hollow Metal Frames | 3 | 0 | 30-May-14 A | 02-Jun-14 A | |

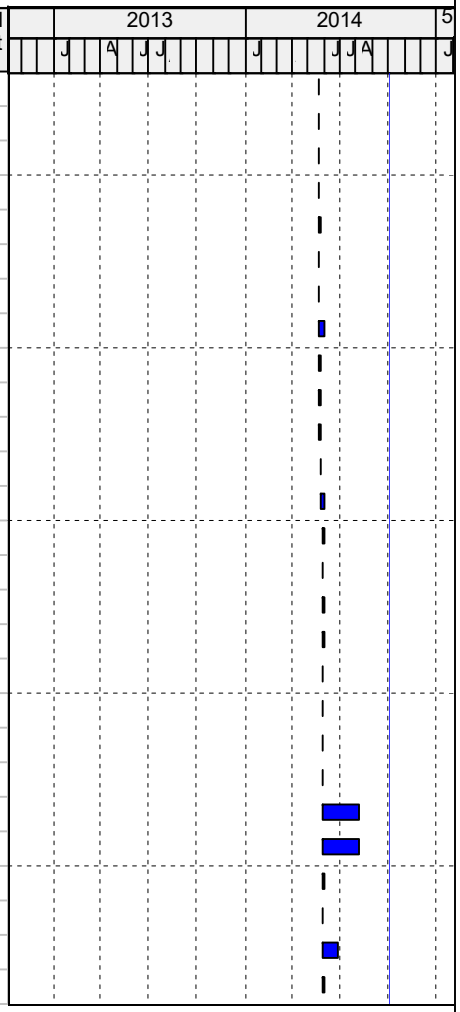


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L17-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L17-8220 | Plumbing Risers - Install | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L10-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L11-6016 | Electrical RI | 5 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L11-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L12-6019 | Complete Top Out GWB | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L14-6020 | Install Hollow Metal Frames | 3 | 0 | 02-Jun-14 A | 05-Jun-14 A | |
| L14-6010 | Frame Walls | 5 | 0 | 02-Jun-14 A | 04-Jun-14 A | |
| L16-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| L14-6019 | Complete Top Out GWB | 2 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L16-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L10-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| L17-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 04-Jun-14 A | 11-Jun-14 A | |
| L08-6016 | Electrical RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L08-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L09-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L12-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L15-6010 | Frame Walls | 3 | 0 | 05-Jun-14 A | 11-Jun-14 A | |
| L09-6012 | Fire Sprinkler Mains | 5 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L09-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L11-6012 | Fire Sprinkler Mains | 4 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L12-6014 | Set Tubs & Plumbing RI | 4 | 0 | 06-Jun-14 A | 27-Jun-14 A | |
| L11-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jun-14 A | 11-Jun-14 A | |
| L09-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-Jun-14 A | 25-Jun-14 A | |
| L14-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L15-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |

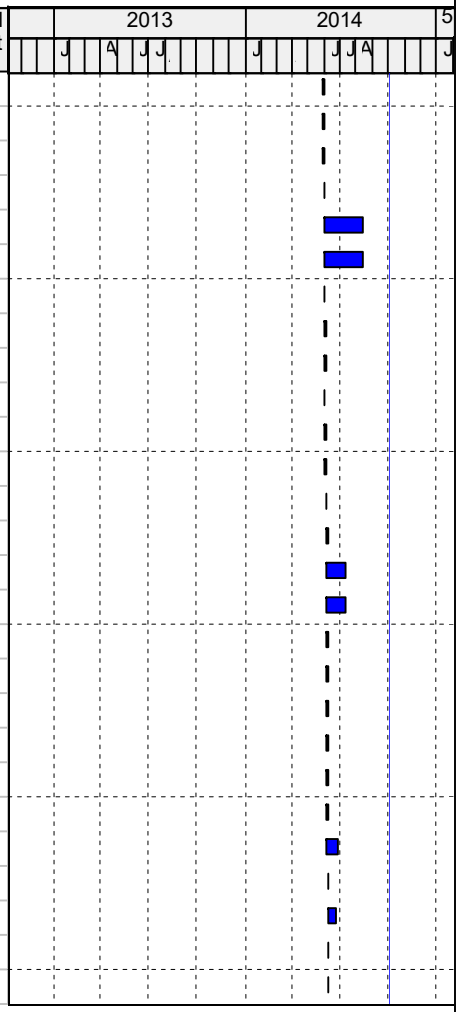



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L09-6016 | Electrical RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L14-6014 | Set Tubs & Plumbing RI | 4 | 0 | 10-Jun-14 A | 21-Jul-14 A | |
| L15-6020 | Install Hollow Metal Frames | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L15-6019 | Complete Top Out GWB | 2 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6014 | Set Tubs & Plumbing RI | 4 | 0 | 11-Jun-14 A | 26-Jun-14 A | |
| L11-6028 | PreRock at Heat Pumps | 2 | 0 | 13-Jun-14 A | 14-Jun-14 A | |
| L11-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 14-Jun-14 A | 14-Jun-14 A | |
| L14-6012 | Fire Sprinkler Mains | 2 | 0 | 16-Jun-14 A | 27-Jun-14 A | |
| L14-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 18-Jun-14 A | 18-Jun-14 A | |
| L15-6023 | Inspection of Exterior Framing | 0 | 0 | 18-Jun-14 A | | |
| L17-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 18-Jun-14 A | 23-Jun-14 A | |
| L17-6010 | Frame Walls | 5 | 0 | 18-Jun-14 A | 29-Jul-14 A | |
| L10-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L12-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6023 | Inspection of Exterior Framing | 0 | 0 | 20-Jun-14 A | | |
| L15-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-Jun-14 A | 20-Jun-14 A | |
| L10-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-Jun-14 A | 23-Jun-14 A | |
| L15-6014 | Set Tubs & Plumbing RI | 5 | 0 | 22-Jun-14 A | 24-Jul-14 A | |
| L08-6018 | HVAC RI | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L12-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |

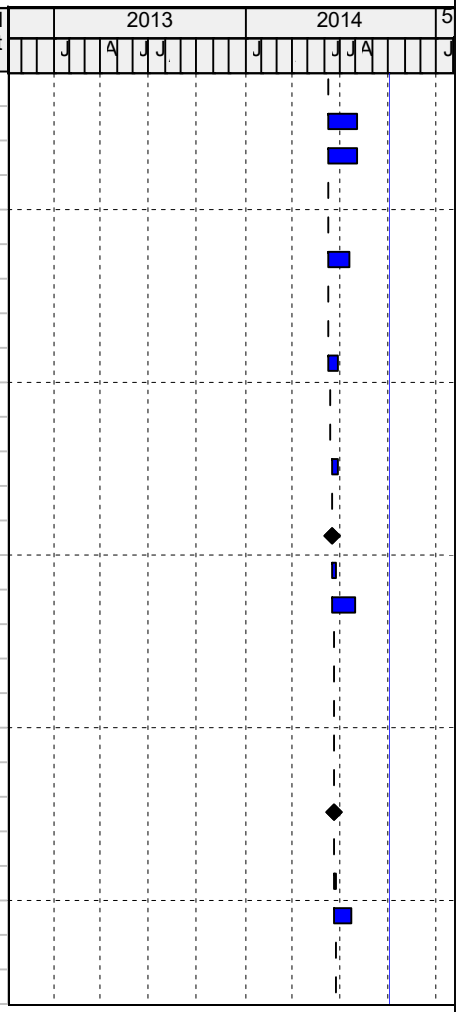


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L15-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L08-6221 | Frame Unit Ceilings | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| L11-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 24-Jun-14 A | 27-Jun-14 A | |
| L12-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L14-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6023 | Inspection of Exterior Framing | 0 | 0 | 24-Jun-14 A | | |
| L12-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| L12-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L14-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L15-6012 | Fire Sprinkler Mains | 2 | 0 | 25-Jun-14 A | 22-Jul-14 A | |
| L16-6023 | Inspection of Exterior Framing | 0 | 0 | 25-Jun-14 A | | |
| L03-6024 | Inspections for GWB Cover | 1 | 0 | 27-Jun-14 A | 27-Jun-14 A | |
| L09-6018 | HVAC RI | 3 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L09-6221 | Frame Unit Ceilings | 2 | 0 | 27-Jun-14 A | 30-Jun-14 A | |
| L12-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L14-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L15-6028 | PreRock at Heat Pumps | 2 | 0 | 30-Jun-14 A | 01-Jul-14 A | |
| L16-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 30-Jun-14 A | 30-Jun-14 A | |
| L16-6010 | Frame Walls | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| L16-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L15-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L15-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L04-6024 | Inspections for GWB Cover | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L10-6018 | HVAC RI | 3 | 0 | 07-Jul-14 A | 21-Jul-14 A | |
| L11-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L15-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |

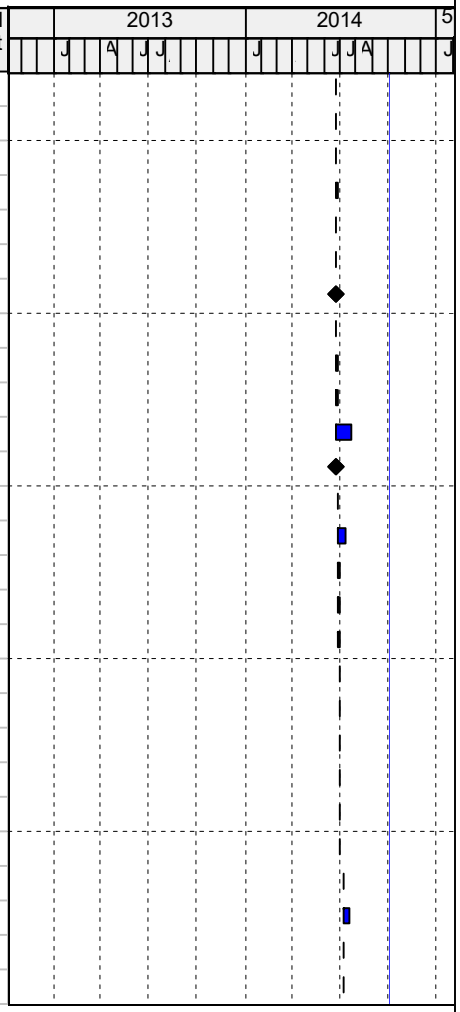


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6012 | Fire Sprinkler Mains | 2 | 0 | 07-Jul-14 A | 24-Jul-14 A | |
| L16-6020 | Install Hollow Metal Frames | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L16-6028 | PreRock at Heat Pumps | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L17-6019 | Complete Top Out GWB | 1 | 0 | 07-Jul-14 A | 08-Aug-14 A | |
| L11-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L15-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 08-Jul-14 A | 04-Aug-14 A | |
| L17-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jul-14 A | 01-Aug-14 A | |
| L10-6221 | Frame Unit Ceilings | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| L17-6012 | Fire Sprinkler Mains | 2 | 0 | 09-Jul-14 A | 12-Aug-14 A | |
| L05-6024 | Inspections for GWB Cover | 2 | 0 | 10-Jul-14 A | 10-Jul-14 A | |
| L04-6000 | Tape/Finish GWB | 6 | 0 | 11-Jul-14 A | 23-Jul-14 A | |
| L16-6019 | Complete Top Out GWB | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L16-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L15-6018 | HVAC RI | 3 | 0 | 16-Jul-14 A | 18-Jul-14 A | |
| L16-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-6024 | Inspections for GWB Cover | 2 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6018 | HVAC RI | 3 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L16-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 21-Jul-14 A | 18-Aug-14 A | |
| L15-6013 | Fire Sprinkler Branch Lines | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| L03-6000 | Tape/Finish GWB | 6 | 0 | 23-Jul-14 A | 29-Jul-14 A | |
| L11-6018 | HVAC RI | 3 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L15-6221 | Frame Unit Ceilings | 2 | 0 | 23-Jul-14 A | 01-Aug-14 A | |
| L16-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L17-6020 | Install Hollow Metal Frames | 3 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| L11-6221 | Frame Unit Ceilings | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |

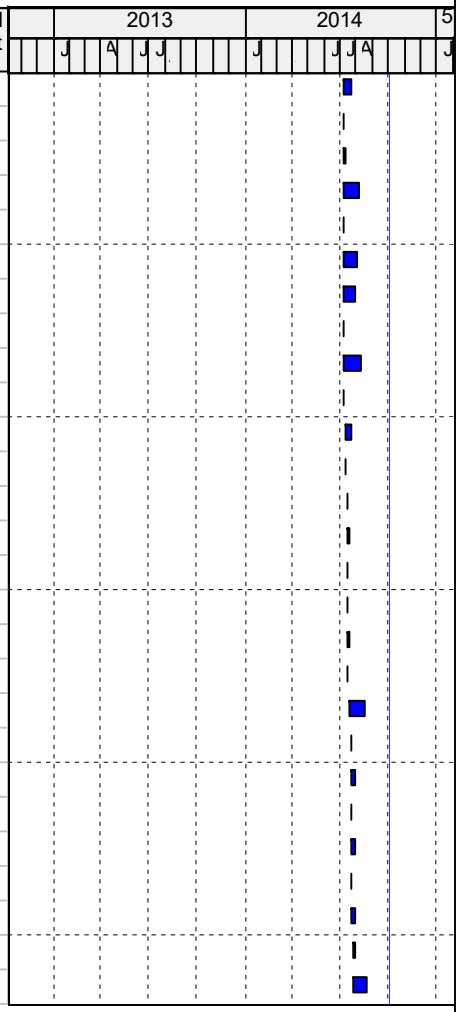


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L14-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L14-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L16-6014 | Set Tubs & Plumbing RI | 5 | 0 | 28-Jul-14 A | 18-Aug-14 A | |
| L07-6024 | Inspections for GWB Cover | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L12-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L05-6000 | Tape/Finish GWB | 6 | 0 | 31-Jul-14 A | 05-Aug-14 A | |
| L08-6024 | Inspections for GWB Cover | 2 | 0 | 31-Jul-14 A | 31-Jul-14 A | |
| L12-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L14-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L06-6000 | Tape/Finish GWB | 4 | 0 | 06-Aug-14 A | 11-Aug-14 A | |
| L09-6024 | Inspections for GWB Cover | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L07-6000 | Tape/Finish GWB | 5 | 0 | 07-Aug-14 A | 16-Aug-14 A | |
| L11-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 08-Aug-14 A | 14-Aug-14 A | |
| L17-6014 | Set Tubs & Plumbing RI | 5 | 0 | 08-Aug-14 A | 16-Sep-14 A | |
| L10-6024 | Inspections for GWB Cover | 2 | 0 | 11-Aug-14 A | 12-Aug-14 A | |
| L09-6000 | Tape/Finish GWB | 5 | 0 | 14-Aug-14 A | 19-Aug-14 A | |
| L08-6000 | Tape/Finish GWB | 5 | 0 | 16-Aug-14 A | 21-Aug-14 A | |
| L11-6024 | Inspections for GWB Cover | 2 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L16-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 18-Aug-14 A | 29-Aug-14 A | |
| L10-6000 | Tape/Finish GWB | 5 | 0 | 19-Aug-14 A | 23-Aug-14 A | |
| L16-6221 | Frame Unit Ceilings | 4 | 0 | 21-Aug-14 A | 26-Aug-14 A | |

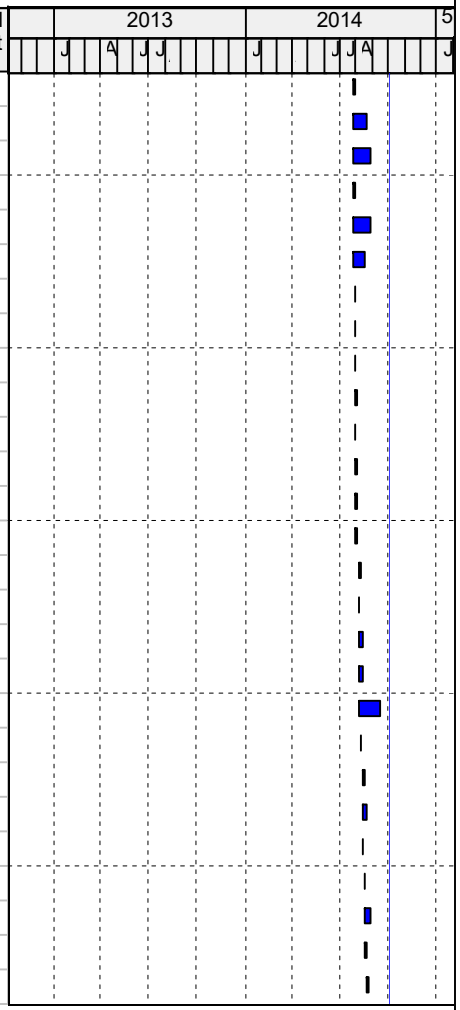



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6018 | HVAC RI | 3 | 0 | 21-Aug-14 A | 10-Sep-14 A | |
| L12-6024 | Inspections for GWB Cover | 2 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L15-6016 | Electrical RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L15-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L11-6000 | Tape/Finish GWB | 5 | 0 | 23-Aug-14 A | 29-Aug-14 A | |
| L17-6221 | Frame Unit Ceilings | 4 | 0 | 26-Aug-14 A | 28-Aug-14 A | |
| L14-6024 | Inspections for GWB Cover | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L16-6016 | Electrical RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L16-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L12-6000 | Tape/Finish GWB | 5 | 0 | 02-Sep-14 A | 08-Sep-14 A | |
| L15-6024 | Inspections for GWB Cover | 2 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L14-6000 | Tape/Finish GWB | 5 | 0 | 06-Sep-14 A | 11-Sep-14 A | |
| L15-6000 | Tape/Finish GWB | 4 | 0 | 12-Sep-14 A | 20-Sep-14 A | |
| L17-6016 | Electrical RI | 5 | 1 | 16-Sep-14 A | 06-Oct-14 | 18 |
| L17-6022 | Fire Alarm / Elec Specialties RI | 5 | 1 | 16-Sep-14 A | 06-Oct-14 | 18 |
| L17-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-6028 | PreRock at Heat Pumps | 2 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L17-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L17-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L17-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 24-Sep-14 A | 27-Sep-14 A | |
| L17-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L16-6024 | Inspections for GWB Cover | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 15 |
| L17-6024 | Inspections for GWB Cover | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 17 |
| L16-6000 | Tape/Finish GWB | 4 | 4 | 11-Oct-14 | 15-Oct-14 | 18 |
| L17-6000 | Tape/Finish GWB | 6 | 6 | 16-Oct-14 | 22-Oct-14 | 18 |

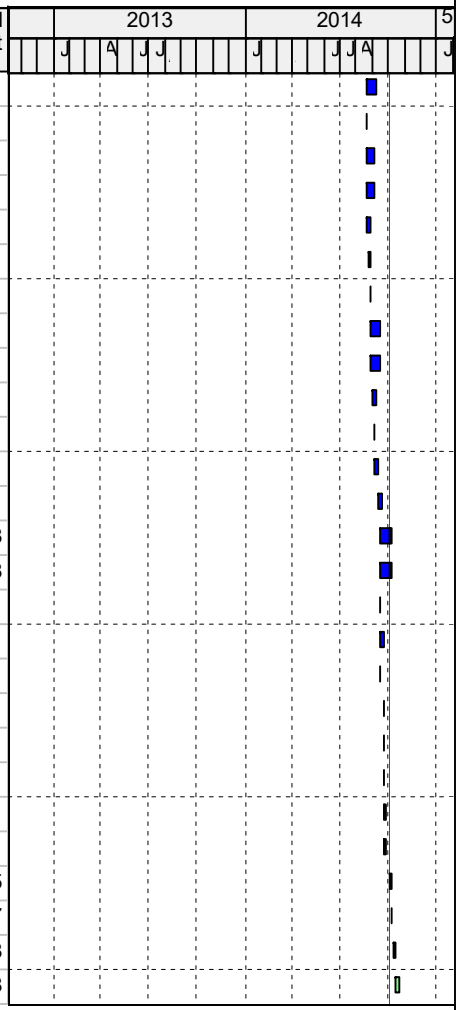



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Mechanical Penthouse** | | | | | | |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 0 | 11-Jun-14 A | 20-Jun-14 A | |
| PH-6006 | PH - Exterior Wall Framing (including PH roof parapet | 6 | 0 | 12-Jun-14 A | 14-Jul-14 A | |
| PH-6014 | PH - Plumbing/Piping RI | 40 | 10 | 25-Jun-14 A | 17-Oct-14 | 4 |
| PH-6002 | PH - Layout | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| PH-6008 | PH - Interior Wall Framing | 3 | 0 | 24-Jul-14 A | 08-Aug-14 A | |
| PH-6020 | PH - H Mtl Frames | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| PH-6016 | PH - Electrical RI | 10 | 10 | 23-Sep-14 A | 17-Oct-14 | 4 |
| PH-6012 | PH - Fire Sprinkler RI | 10 | 10 | 06-Oct-14 | 17-Oct-14 | 24 |
| PH-6018 | PH - HVAC RI | 10 | 10 | 06-Oct-14 | 17-Oct-14 | 24 |
| PH-6022 | PH - Fire Alarm / Elec Specialties RI | 10 | 10 | 06-Oct-14 | 17-Oct-14 | 24 |
| PH-6024 | PH - Inspections | 2 | 2 | 20-Oct-14 | 21-Oct-14 | 24 |
| **Finishes** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL4-8100 | LL4 - Insulation | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 41 |
| LL4-8102 | LL4 - GWB Hang (incl. screw inspection) | 4 | 4 | 08-Oct-14 | 11-Oct-14 | 49 |
| LL4-8104 | LL4 - Int Painting | 2 | 2 | 17-Oct-14 | 20-Oct-14 | 42 |
| LL4-8122 | LL4 - Plumbing Trim / Finish | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 49 |
| LL4-8108 | LL4 - Elec Trim / Finish | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 49 |
| LL4-8110 | LL4 - HVAC Trim / Finish | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 49 |
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 43 |
| LL4-8124 | LL4 - Flooring (VCT) | 4 | 4 | 21-Oct-14 | 24-Oct-14 | 42 |
| LL4-8118 | LL4 - Elec Specialties Trim / Finish | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 43 |
| LL4-8126 | LL4 - Doors & Hardware | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 42 |
| LL4-8114 | LL4 - Striping / Signage | 5 | 5 | 28-Oct-14 | 03-Nov-14 | 42 |

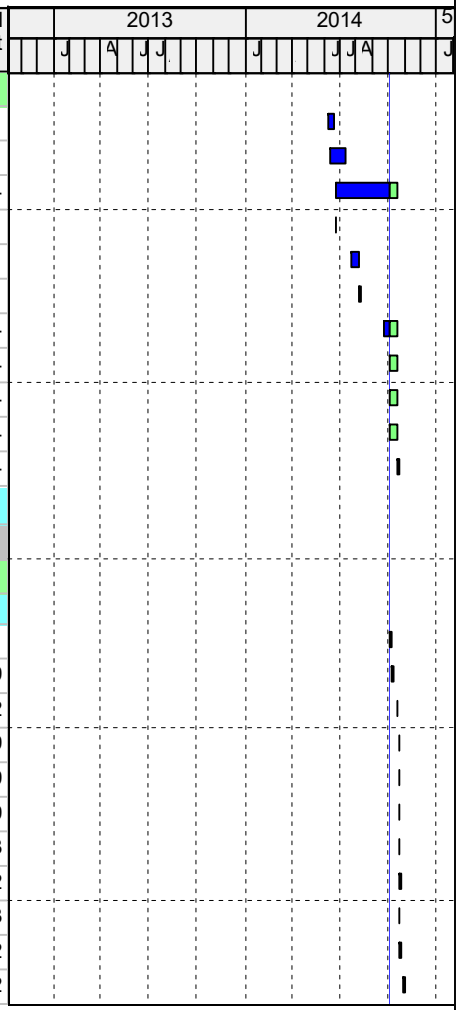



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8132 | LL4 - Punch | 5 | 5 | 04-Nov-14 | 10-Nov-14 | 42 |
| LL4-8134 | LL4 - Clean | 5 | 5 | 04-Nov-14 | 10-Nov-14 | 42 |
| LL4-8210 | LL4 - Owner Walk / Create Punchlist | 1 | 1 | 11-Nov-14 | 11-Nov-14 | 42 |
| LL4-8212 | LL4 - Resolve Final Punchlist | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 42 |
| LL4-8214 | LL4 - Floor Complete | 0 | 0 | | 18-Nov-14 | 42 |
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL3-8100 | LL3 - Insulation | 2 | 2 | 06-Oct-14 | 07-Oct-14 | 49 |
| LL3-8102 | LL3 - GWB Hang (incl. screw inspection) | 4 | 4 | 08-Oct-14 | 11-Oct-14 | 49 |
| LL3-8104 | LL3 - Int Painting | 2 | 2 | 17-Oct-14 | 20-Oct-14 | 42 |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 49 |
| LL3-8108 | LL3 - Elec Trim / Finish | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 49 |
| LL3-8110 | LL3 - HVAC Trim / Finish | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 49 |
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 43 |
| LL3-8124 | LL3 - Flooring (VCT) | 4 | 4 | 21-Oct-14 | 24-Oct-14 | 42 |
| LL3-8118 | LL3 - Elec Specialties Trim / Finish | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 43 |
| LL3-8126 | LL3 - Doors & Hardware | 3 | 3 | 23-Oct-14 | 27-Oct-14 | 42 |
| LL3-8114 | LL3 - Striping / Signage | 5 | 5 | 28-Oct-14 | 03-Nov-14 | 42 |
| LL3-8132 | LL3 - Punch | 5 | 5 | 04-Nov-14 | 10-Nov-14 | 42 |
| LL3-8134 | LL3 - Clean | 5 | 5 | 04-Nov-14 | 10-Nov-14 | 42 |
| LL3-8210 | LL3 - Owner Walk / Create Punchlist | 1 | 1 | 11-Nov-14 | 11-Nov-14 | 42 |
| LL3-8212 | LL3 - Resolve Final Punchlist | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 42 |
| LL3-8214 | LL3 - Floor Complete | 0 | 0 | | 18-Nov-14 | 42 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL2E-8102 | LL2 - GWB Hang / Tape / Finish @ Electrical Rooms | 8 | 0 | 24-Jun-14 A | 03-Jul-14 A | |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish & Inspection | 6 | 5 | 16-Sep-14 A | 14-Oct-14 | 46 |

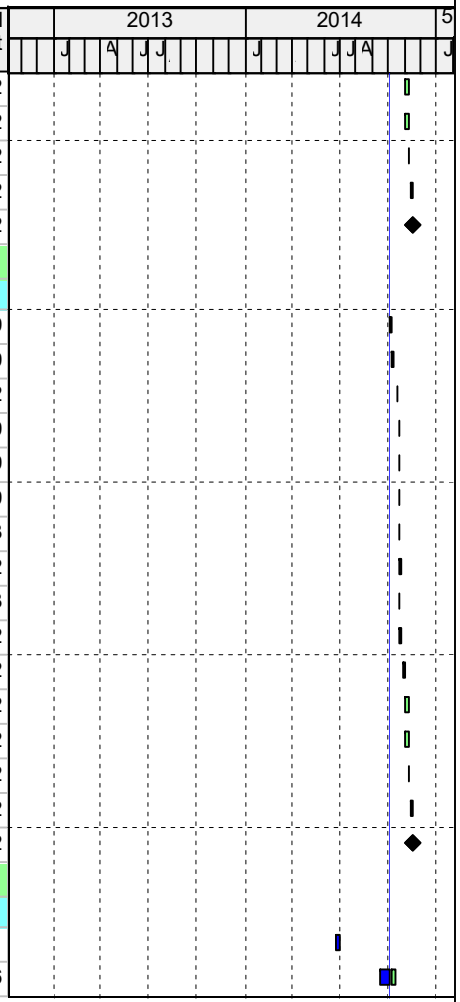


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-8100 | LL2 - Insulation | 5 | 3 | 16-Sep-14 A | 11-Oct-14 | 46 |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 5 | 4 | 17-Sep-14 A | 14-Oct-14 | 39 |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 52 |
| LL2-8104 | LL2 - Int Painting | 4 | 4 | 15-Oct-14 | 20-Oct-14 | 39 |
| LL2-8128 | LL2 - Entry Gates | 3 | 3 | 16-Oct-14 | 20-Oct-14 | 52 |
| LL2-8116 | LL2 - Finish Carpentry / Millwork | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 50 |
| LL2-8122 | LL2 - Plumbing Trim / Finish | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 39 |
| LL2-8108 | LL2 - Elec Trim / Finish | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 39 |
| LL2-8110 | LL2 - HVAC Trim / Finish | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 39 |
| LL2-8112 | LL2 - Fire Sprinkler Trim / Finish | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 39 |
| LL2-8124 | LL2 - Flooring | 4 | 4 | 21-Oct-14 | 24-Oct-14 | 39 |
| LL2-8118 | LL2 - Elec Specialties Trim / Finish | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 39 |
| LL2-8120 | LL2 - Install Bollards | 3 | 3 | 21-Oct-14 | 23-Oct-14 | 49 |
| LL2-8136 | LL2 - Chainlink Fencing / Gate @ Recycling | 5 | 5 | 24-Oct-14 | 30-Oct-14 | 39 |
| LL2-8126 | LL2 - Doors & Hardware | 4 | 4 | 27-Oct-14 | 30-Oct-14 | 39 |
| LL2-8114 | LL2 - Striping / Signage | 5 | 5 | 31-Oct-14 | 06-Nov-14 | 39 |
| LL2-8132 | LL2 - Punch | 5 | 5 | 07-Nov-14 | 13-Nov-14 | 39 |
| LL2-8134 | LL2 - Clean | 5 | 5 | 07-Nov-14 | 13-Nov-14 | 39 |
| LL2-8210 | LL2 - Owner Walk / Create Punchlist | 1 | 1 | 14-Nov-14 | 14-Nov-14 | 39 |
| LL2-8212 | LL2 - Resolve Final Punchlist | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 39 |
| LL2-8214 | LL2 - Floor Complete | 0 | 0 | | 21-Nov-14 | 39 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 31-Jul-14 A | |
| LL1-Z2U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 09-May-14 A | |
| LL1-Z3U-8102 | Above Ceiling GWB (At All Areas North of Q-Line) | 5 | 0 | 10-Feb-14 A | 20-Jun-14 A | |
| L1BU-8102 | Above Ceiling GWB [including East Service Corridor] | 5 | 0 | 06-Jun-14 A | 11-Jun-14 A | |

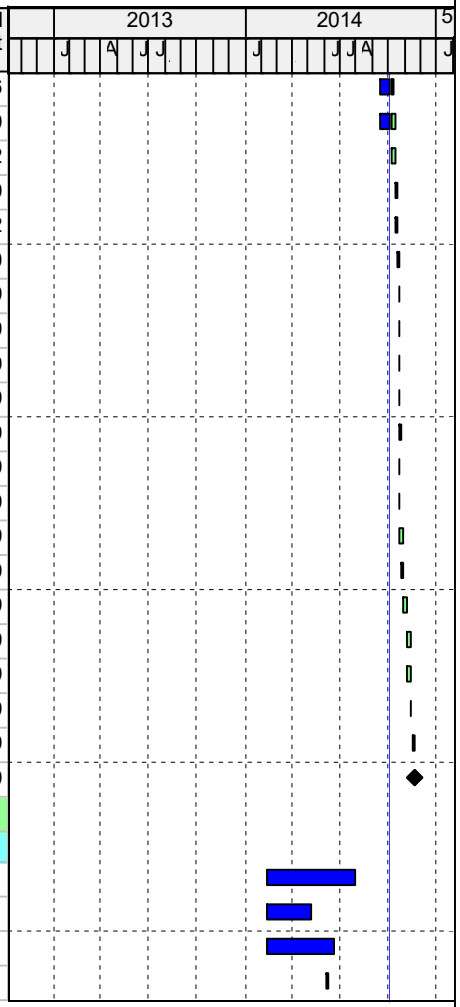


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1LU-8102 | Above Ceiling GWB | 5 | 2 | 24-Jun-14 A | 08-Oct-14 | 0 |
| L1KU-8102 | Above Ceiling GWB | 2 | 0 | 26-Jun-14 A | 22-Aug-14 A | |
| LL1-8100 | Insulation | 5 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| LL1-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 28-Jul-14 A | 06-Aug-14 A | |
| LL1-Z2-8102 | GWB Hang (Walls) & Inspection | 4 | 0 | 11-Aug-14 A | 14-Aug-14 A | |
| LL1-Z2-8100 | Insulation | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| LL1-8215 | GWB Tape (Walls) | 10 | 10 | 16-Aug-14 A | 16-Oct-14 | 22 |
| LL1-Z3-8102 | GWB Hang (Walls) & Inspection | 5 | 2 | 15-Sep-14 A | 07-Oct-14 | 26 |
| LL1-Z3-8100 | Insulation | 5 | 0 | 15-Sep-14 A | 24-Sep-14 A | |
| LL1-Z2-8215 | GWB Tape (Walls/Ceilings) | 7 | 5 | 29-Sep-14 A | 28-Oct-14 | 19 |
| LL1-8114 | T Bar Grid Ceiling & Inspection | 7 | 4 | 29-Sep-14 A | 04-Nov-14 | 23 |
| L1B-8100 | Insulation | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 2 |
| L1K-8100 | Insulation | 5 | 5 | 06-Oct-14 | 10-Oct-14 | 13 |
| L1B-8102 | GWB Hang (Walls) & Inspection - Main Ballroom N/S/ | 4 | 4 | 07-Oct-14 | 10-Oct-14 | 2 |
| L1K-8102 | GWB Hang (Walls) & Inspection | 8 | 8 | 07-Oct-14 | 15-Oct-14 | 15 |
| LL1-Z3-8215 | GWB Tape (Walls & Ceilings) | 7 | 7 | 09-Oct-14 | 17-Oct-14 | 26 |
| L1L-8100 | Insulation | 4 | 4 | 13-Oct-14 | 16-Oct-14 | 0 |
| L1L-8102 | GWB Hang (Walls) | 4 | 4 | 14-Oct-14 | 17-Oct-14 | 0 |
| L1B-8215 | GWB Tape (Walls) | 6 | 6 | 15-Oct-14 | 21-Oct-14 | 2 |
| L1K-8215 | GWB Tape (Walls & Ceilings) | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 12 |
| LL1-Z3-8104 | Prime Paint | 2 | 2 | 20-Oct-14 | 21-Oct-14 | 26 |
| L1L-8215 | GWB Tape (Walls) | 7 | 7 | 20-Oct-14 | 28-Oct-14 | 0 |
| LL1-Z3-8114 | T Bar Grid Ceiling & Inspection | 6 | 6 | 22-Oct-14 | 29-Oct-14 | 26 |
| L1K-8104 | Prime Paint | 4 | 4 | 23-Oct-14 | 28-Oct-14 | 12 |
| LL1-8104 | Prime Paint | 3 | 3 | 29-Oct-14 | 31-Oct-14 | 19 |
| LL1-Z2-8104 | Prime Paint | 2 | 2 | 29-Oct-14 | 30-Oct-14 | 19 |
| L1K-8106 | Wallcoverings (FRP) | 1 | 1 | 29-Oct-14 | 29-Oct-14 | 12 |

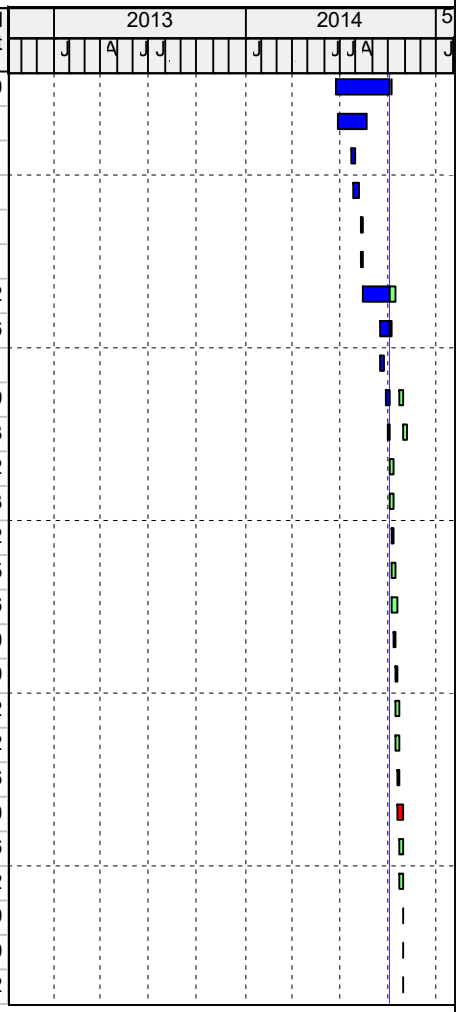



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8114 | T Bar Grid Ceiling | 4 | 4 | 29-Oct-14 | 03-Nov-14 | 20 |
| LL1-Z2-8114 | T Bar Grid Ceiling & Inspection | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 19 |
| LL1-Z3-8140 | Acoustical Ceiling Tile | 5 | 5 | 05-Nov-14 | 11-Nov-14 | 26 |
| LL1-Z2-8106 | Wallcoverings | 4 | 4 | 06-Nov-14 | 11-Nov-14 | 19 |
| LL1-Z3-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 07-Nov-14 | 11-Nov-14 | 26 |
| LL1-Z3-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 07-Nov-14 | 11-Nov-14 | 26 |
| LL1-Z2-8124 | Flooring | 5 | 5 | 11-Nov-14 | 17-Nov-14 | 19 |
| L1K-8140 | Acoustical Ceiling Tile | 4 | 4 | 11-Nov-14 | 14-Nov-14 | 12 |
| LL1-8124 | Flooring | 6 | 6 | 12-Nov-14 | 19-Nov-14 | 20 |
| LL1-Z3-8124 | Flooring (Epoxy) | 9 | 9 | 12-Nov-14 | 20-Nov-14 | 38 |
| L1K-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 13-Nov-14 | 17-Nov-14 | 12 |
| L1K-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 13-Nov-14 | 17-Nov-14 | 12 |
| L1K-8124 | Flooring (VCT & Tile) | 3 | 3 | 14-Nov-14 | 18-Nov-14 | 12 |
| LL1-Z2-8116 | Finish Carpentry / Millwork | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 19 |
| LL1-Z2-8126 | Doors & Hardware | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 22 |
| LL1-8116 | Finish Carpentry / Millwork | 5 | 5 | 19-Nov-14 | 25-Nov-14 | 20 |
| LL1-8126 | Doors & Hardware | 5 | 5 | 19-Nov-14 | 25-Nov-14 | 21 |
| LL1-8140 | Acoustical Ceiling Tile | 5 | 5 | 19-Nov-14 | 25-Nov-14 | 20 |
| LL1-Z2-8140 | Acoustical Ceiling Tile | 3 | 3 | 20-Nov-14 | 24-Nov-14 | 19 |
| LL1-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 21-Nov-14 | 25-Nov-14 | 20 |
| LL1-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 21-Nov-14 | 25-Nov-14 | 20 |
| LL1-Z3-8116 | Finish Carpentry / Millwork | 4 | 4 | 21-Nov-14 | 26-Nov-14 | 23 |
| LL1-Z3-8126 | Doors & Hardware | 5 | 5 | 21-Nov-14 | 01-Dec-14 | 22 |
| LL1-Z2-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 20 |
| LL1-Z2-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 19 |
| L1B-8104 | Prime Paint | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 1 |
| L1K-8116 | Finish Carpentry / Millwork | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 12 |

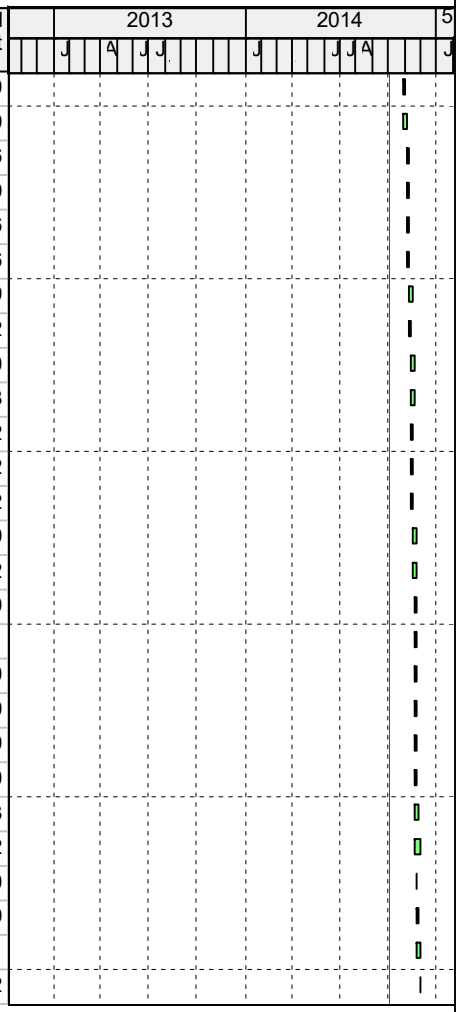



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8126 | Doors & Hardware | 5 | 5 | 01-Dec-14 | 05-Dec-14 | 12 |
| L1B-8114 | T Bar Grid Ceiling | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 1 |
| L1L-8104 | Prime Paint | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 0 |
| LL1-8132 | Punch | 5 | 5 | 05-Dec-14 | 11-Dec-14 | 21 |
| LL1-8134 | Clean | 5 | 5 | 05-Dec-14 | 11-Dec-14 | 21 |
| LL1-Z2-8132 | Punch | 5 | 5 | 08-Dec-14 | 12-Dec-14 | 20 |
| LL1-Z2-8134 | Clean | 5 | 5 | 08-Dec-14 | 12-Dec-14 | 20 |
| LL1-Z3-8132 | Punch | 4 | 4 | 09-Dec-14 | 12-Dec-14 | 22 |
| LL1-Z3-8134 | Clean | 4 | 4 | 09-Dec-14 | 12-Dec-14 | 22 |
| L1L-8114 | Install wood ceiling supports | 2 | 2 | 09-Dec-14 | 10-Dec-14 | 0 |
| L1L-8106 | Wallcoverings | 5 | 5 | 11-Dec-14 | 17-Dec-14 | 0 |
| L1B-8124 | Flooring (Carpet) | 4 | 4 | 12-Dec-14 | 17-Dec-14 | 1 |
| L1K-8132 | Punch | 5 | 5 | 12-Dec-14 | 18-Dec-14 | 12 |
| L1K-8134 | Clean | 5 | 5 | 12-Dec-14 | 18-Dec-14 | 12 |
| L1B-8116 | Finish Carpentry / Millwork | 4 | 4 | 18-Dec-14 | 23-Dec-14 | 4 |
| L1B-8126 | Doors & Hardware | 4 | 4 | 18-Dec-14 | 23-Dec-14 | 4 |
| L1B-8140 | Acoustical Ceiling Tile | 4 | 4 | 18-Dec-14 | 23-Dec-14 | 1 |
| L1L-8124 | Flooring | 5 | 5 | 18-Dec-14 | 24-Dec-14 | 0 |
| L1B-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 23-Dec-14 | 30-Dec-14 | 1 |
| L1B-8118 | Elec & Specialties Trim / Finish | 4 | 4 | 23-Dec-14 | 30-Dec-14 | 1 |
| L1L-8140 | Install wood ceiling | 6 | 6 | 23-Dec-14 | 02-Jan-15 | 0 |
| L1L-8116 | Finish Carpentry / Millwork | 4 | 4 | 29-Dec-14 | 02-Jan-15 | 0 |
| L1L-8126 | Doors & Hardware | 4 | 4 | 29-Dec-14 | 02-Jan-15 | 0 |
| L1L-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 31-Dec-14 | 02-Jan-15 | 0 |
| L1L-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 31-Dec-14 | 02-Jan-15 | 0 |
| L1B-8132 | Punch | 4 | 4 | 08-Jan-15 | 13-Jan-15 | 1 |
| L1B-8134 | Clean | 4 | 4 | 08-Jan-15 | 13-Jan-15 | 1 |

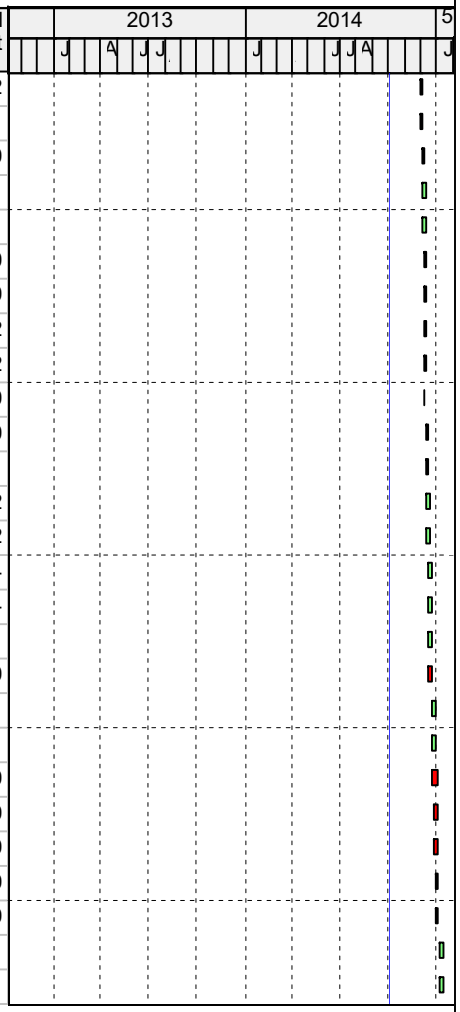



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8132 | Punch | 4 | 4 | 12-Jan-15 | 15-Jan-15 | 0 |
| L1L-8134 | Clean | 4 | 4 | 12-Jan-15 | 15-Jan-15 | 0 |
| **Corridors / Common / Public Areas** | | | | | | |
| LL1-Z3-8200 | First Coat Finish Paint | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 26 |
| LL1-Z2-8200 | First Coat Finish Paint | 5 | 5 | 04-Nov-14 | 10-Nov-14 | 19 |
| L1K-8200 | First Coat Finish Paint | 5 | 5 | 04-Nov-14 | 10-Nov-14 | 12 |
| LL1-8200 | First Coat Finish Paint | 5 | 5 | 05-Nov-14 | 11-Nov-14 | 20 |
| LL1-Z3-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 07-Nov-14 | 11-Nov-14 | 26 |
| L1K-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 13-Nov-14 | 17-Nov-14 | 12 |
| LL1-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 21-Nov-14 | 25-Nov-14 | 20 |
| LL1-Z2-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 19 |
| LL1-8201 | Final Coat Finish Paint | 5 | 5 | 26-Nov-14 | 04-Dec-14 | 21 |
| LL1-Z2-8201 | Final Coat Finish Paint | 5 | 5 | 01-Dec-14 | 05-Dec-14 | 20 |
| LL1-Z3-8201 | Final Coat Finish Paint | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 22 |
| L1B-8200 | First Coat Finish Paint | 5 | 5 | 05-Dec-14 | 11-Dec-14 | 1 |
| L1K-8201 | Final Coat Finish Paint | 4 | 4 | 08-Dec-14 | 11-Dec-14 | 12 |
| L1L-8200 | First Coat Finish Paint | 5 | 5 | 11-Dec-14 | 17-Dec-14 | 0 |
| LL1-8210 | Owner Walk / Create Punchlist | 1 | 1 | 12-Dec-14 | 12-Dec-14 | 21 |
| LL1-8212 | Resolve Final Punchlist | 5 | 5 | 15-Dec-14 | 19-Dec-14 | 21 |
| LL1-Z2-8210 | Owner Walk / Create Punchlist | 1 | 1 | 15-Dec-14 | 15-Dec-14 | 20 |
| LL1-Z3-8210 | Owner Walk / Create Punchlist | 1 | 1 | 15-Dec-14 | 15-Dec-14 | 22 |
| LL1-Z2-8212 | Resolve Final Punchlist | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 20 |
| LL1-Z3-8212 | Resolve Final Punchlist | 3 | 3 | 16-Dec-14 | 18-Dec-14 | 22 |
| LL1-Z3-8214 | LL1, Zone 3 Complete | 0 | 0 | | 18-Dec-14 | 22 |
| L1K-8210 | Owner Walk / Create Punchlist | 1 | 1 | 19-Dec-14 | 19-Dec-14 | 17 |
| LL1-8214 | LL1, Zone 1 Complete | 0 | 0 | | 19-Dec-14 | 21 |
| L1K-8212 | Resolve Final Punchlist | 4 | 4 | 22-Dec-14 | 29-Dec-14 | 17 |

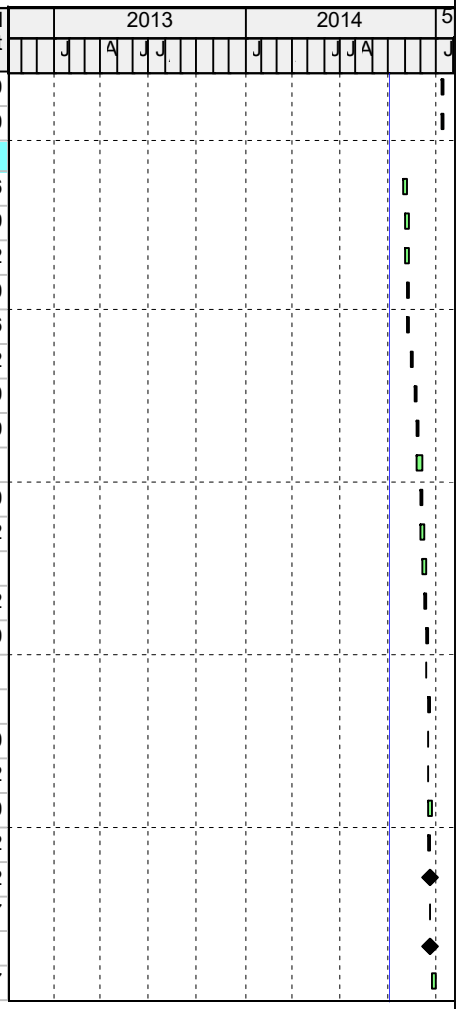


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-8214 | LL1 Zone 2 Compllete | 0 | 0 | | 22-Dec-14 | 20 |
| L1B-8204 | Mech Trim / Finish (HVAC & Plumbing) | 4 | 4 | 23-Dec-14 | 30-Dec-14 | 1 |
| L1B-8201 | Final Coat Finish Paint | 5 | 5 | 31-Dec-14 | 07-Jan-15 | 1 |
| L1L-8204 | Mech Trim / Finish (HVAC & Plumbing) | 2 | 2 | 31-Dec-14 | 02-Jan-15 | 0 |
| L1L-8201 | Final Coat Finish Paint | 5 | 5 | 05-Jan-15 | 09-Jan-15 | 0 |
| L1K-8214 | L1, Zone 1 Complete | 0 | 0 | | 06-Jan-15 | 12 |
| L1B-8210 | Owner Walk / Create Punchlist | 1 | 1 | 14-Jan-15 | 14-Jan-15 | 1 |
| L1B-8212 | Resolve Final Punchlist | 5 | 5 | 15-Jan-15 | 21-Jan-15 | 1 |
| L1L-8210 | Owner Walk / Create Punchlist | 1 | 1 | 16-Jan-15 | 16-Jan-15 | 0 |
| L1L-8212 | Resolve Final Punchlist | 4 | 4 | 19-Jan-15 | 22-Jan-15 | 0 |
| L1B-8214 | L1, Zone 2 Complete | 0 | 0 | | 21-Jan-15 | 1 |
| L1L-8214 | L1, Zone 4 Complete | 0 | 0 | | 22-Jan-15 | 0 |
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8102 | L2 - GWB Hang / Tape / Finish - North Half | 7 | 7 | 14-Oct-14 | 21-Oct-14 | 30 |
| L02-8100 | L2 - Insulation - North Half | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 25 |
| L02-8104 | L2 - Int Painting - North Half | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 30 |
| L02-8106 | L2 - Wallcoverings | 4 | 4 | 27-Oct-14 | 30-Oct-14 | 25 |
| L02-8124 | L2 - Flooring | 5 | 5 | 31-Oct-14 | 06-Nov-14 | 25 |
| L02-8108 | L2 - Elec Trim / Finish | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 31 |
| L02-8110 | L2 - HVAC Trim / Finish | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 31 |
| L02-8112 | L2 - Fire Sprinkler Trim / Finish | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 31 |
| L02-8118 | L2 - Elec Specialties Trim / Finish | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 31 |
| L02-8116 | L2 - Finish Carpentry / Millwork | 4 | 4 | 06-Nov-14 | 11-Nov-14 | 25 |
| L02-8120 | L2 - Ceramic Tile / Counter Tops | 5 | 5 | 06-Nov-14 | 12-Nov-14 | 25 |
| L02-8128 | L2 - Bath Specialties | 4 | 4 | 06-Nov-14 | 11-Nov-14 | 31 |
| L02-8122 | L2 - Plumbing Trim / Finish | 5 | 5 | 10-Nov-14 | 14-Nov-14 | 33 |

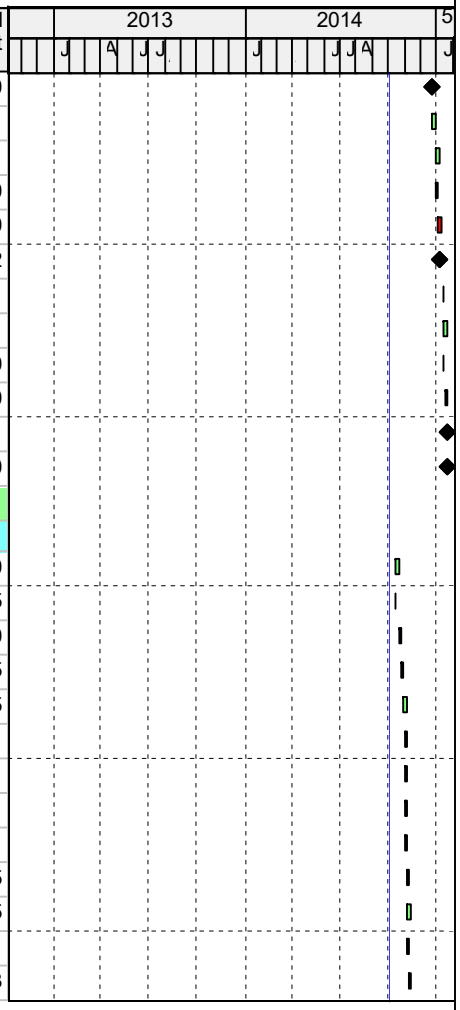



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8126 | L2 - Doors & Hardware | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 26 |
| L02-8136 | L2 - Lockers / Benches @ Locker Rooms | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 25 |
| L02-8132 | L2 - Punch | 5 | 5 | 01-Dec-14 | 05-Dec-14 | 25 |
| L02-8134 | L2 - Clean | 5 | 5 | 01-Dec-14 | 05-Dec-14 | 25 |
| **Corridors** | | | | | | |
| L02-8200 | L2 - Final Paint @ Common / Public Areas | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 25 |
| L02-8114 | L2 - Signage | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 27 |
| L02-8210 | L2 - Owner Walk / Create Punchlist | 1 | 1 | 08-Dec-14 | 08-Dec-14 | 25 |
| L02-8212 | L2 - Resolve Final Punchlist | 5 | 5 | 09-Dec-14 | 15-Dec-14 | 25 |
| L02-8214 | L2 - Floor Complete | 0 | 0 | | 15-Dec-14 | 25 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L03-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L04-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L05-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L06-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L07-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L08-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L09-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L10-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L11-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L12-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L14-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L15-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L16-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L17-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |

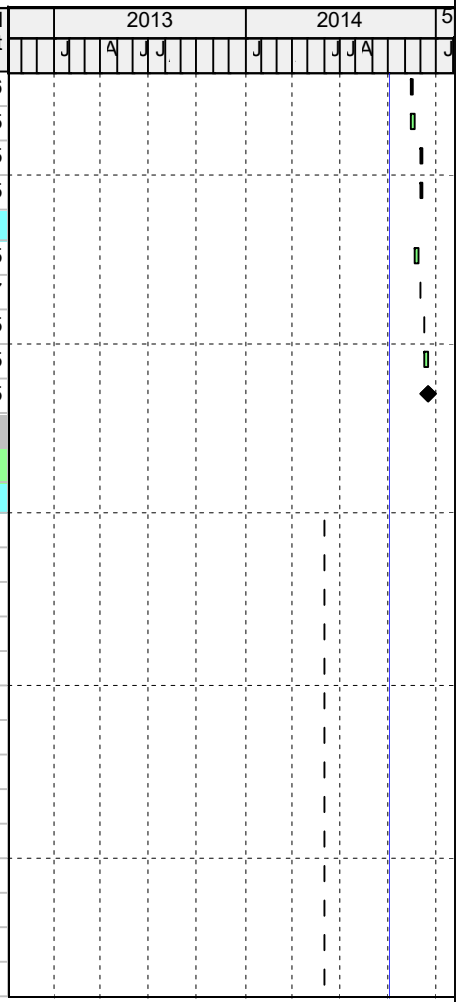



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8102S | Stock GWB | 2 | 0 | 27-Jun-14 A | 08-Jul-14 A | |
| L04-8102 | Hang GWB & Inspection | 4 | 0 | 07-Jul-14 A | 16-Jul-14 A | |
| L04-8102S | Stock GWB | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-8102 | Hang GWB & Inspection | 5 | 0 | 09-Jul-14 A | 22-Jul-14 A | |
| L05-8102S | Stock GWB | 2 | 0 | 10-Jul-14 A | 14-Jul-14 A | |
| L05-8102 | Hang GWB & Inspection | 4 | 0 | 17-Jul-14 A | 23-Jul-14 A | |
| L06-8102S | Stock GWB | 2 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L04-8104 | Paint (Prime) | 2 | 0 | 28-Jul-14 A | 05-Aug-14 A | |
| L03-8104 | Paint (Prime) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L03-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L07-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L08-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L06-8102 | Hang GWB & Inspection | 5 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L07-8102 | Hang GWB & Inspection | 6 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L04-8105 | Paint (First Coat & Ceilings) | 5 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L05-8104 | Paint (Prime) | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| L09-8102S | Stock GWB | 2 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 07-Aug-14 A | 11-Aug-14 A | |
| L09-8102 | Hang GWB & Inspection | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| L08-8102 | Hang GWB & Inspection | 6 | 0 | 11-Aug-14 A | 15-Aug-14 A | |
| L06-8104 | Paint (Prime) | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L10-8102S | Stock GWB | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-8102 | Hang GWB & Inspection | 4 | 0 | 13-Aug-14 A | 18-Aug-14 A | |
| L06-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 14-Aug-14 A | 18-Aug-14 A | |
| L11-8102S | Stock GWB | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L07-8104 | Paint (Prime) | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L11-8102 | Hang GWB & Inspection | 4 | 0 | 18-Aug-14 A | 22-Aug-14 A | |

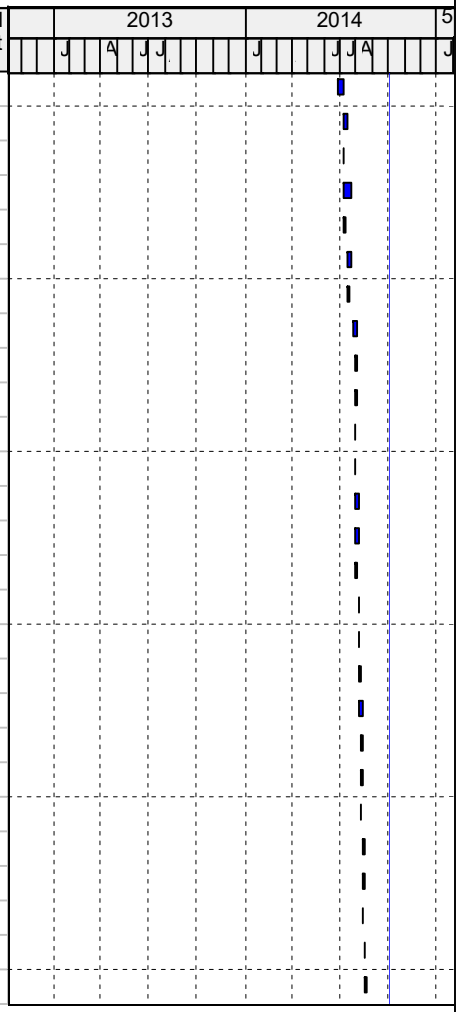



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8105 | Paint (First Coat & Ceilings) | 4 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L09-8104 | Paint (Prime) | 2 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L08-8104 | Paint (Prime) | 2 | 0 | 22-Aug-14 A | 25-Aug-14 A | |
| L12-8102 | Hang GWB & Inspection | 4 | 0 | 22-Aug-14 A | 30-Aug-14 A | |
| L12-8102S | Stock GWB | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8108 | Elec Trim / Finish | 4 | 0 | 25-Aug-14 A | 04-Sep-14 A | |
| L08-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L03-8118 | Fire Alarm Trim / Finish | 3 | 0 | 27-Aug-14 A | 29-Sep-14 A | |
| L14-8102S | Stock GWB | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L09-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 29-Aug-14 A | 09-Sep-14 A | |
| L14-8102 | Hang GWB & Inspection | 5 | 0 | 29-Aug-14 A | 05-Sep-14 A | |
| L03-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 02-Sep-14 A | 05-Sep-14 A | |
| L04-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 04-Sep-14 A | 09-Sep-14 A | |
| L10-8104 | Paint (Prime) | 2 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| L15-8102S | Stock GWB | 1 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L15-8102 | Hang GWB & Inspection | 5 | 0 | 06-Sep-14 A | 12-Sep-14 A | |
| L03-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8108 | Elec Trim / Finish | 4 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L04-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 11-Sep-14 A | |
| L05-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 08-Sep-14 A | 12-Sep-14 A | |
| L10-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 08-Sep-14 A | 12-Sep-14 A | |
| L11-8104 | Paint (Prime) | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L04-8116 | Install Base at Guestrooms | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L11-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 10-Sep-14 A | 22-Sep-14 A | |
| L03-8116 | Install Base at Guestrooms | 5 | 0 | 12-Sep-14 A | 16-Sep-14 A | |
| L12-8104 | Paint (Prime) | 2 | 0 | 12-Sep-14 A | 17-Sep-14 A | |

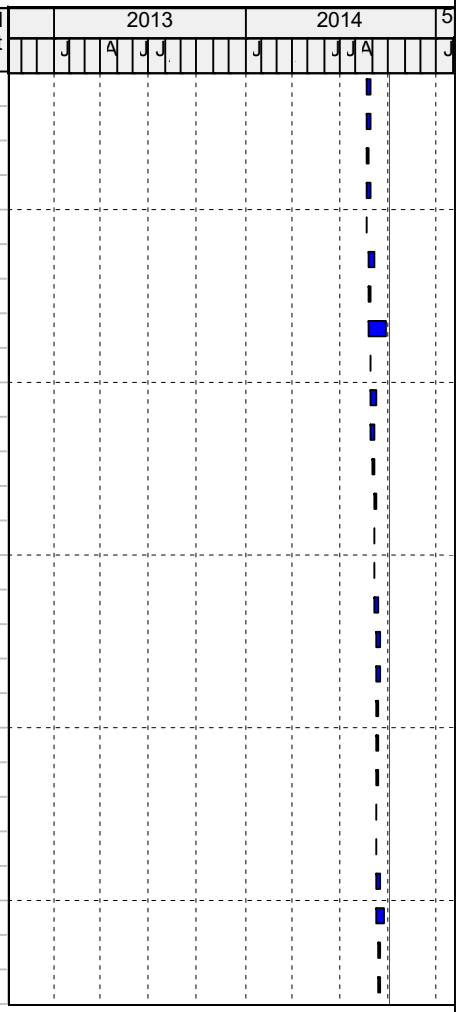



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8116 | Install Base at Guestrooms | 5 | 0 | 16-Sep-14 A | 24-Sep-14 A | |
| L06-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L05-8108 | Elec Trim / Finish | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L07-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 17-Sep-14 A | 23-Sep-14 A | |
| L12-8105 | Paint (First Coat & Ceilings) | 3 | 1 | 17-Sep-14 A | 06-Oct-14 | 21 |
| L06-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L07-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L14-8104 | Paint (Prime) | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L06-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L06-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L08-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L14-8105 | Paint (First Coat & Ceilings) | 3 | 1 | 24-Sep-14 A | 06-Oct-14 | 23 |
| L15-8104 | Paint (Prime) | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L03-8110 | HVAC Trim / Finish (including Corridors) | 3 | 1 | 29-Sep-14 A | 06-Oct-14 | 60 |
| L03-8120 | Install Countertops/Sills | 3 | 1 | 29-Sep-14 A | 06-Oct-14 | 17 |
| L04-8120 | Install Countertops/Sills | 3 | 1 | 29-Sep-14 A | 06-Oct-14 | 17 |
| L04-8118 | Fire Alarm Trim / Finish | 3 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L09-8118 | Fire Alarm Trim / Finish | 3 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L10-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L08-8124 | Guestroom/Bathroom Flooring | 5 | 1 | 30-Sep-14 A | 06-Oct-14 | 30 |
| L03-8126 | Doors & Hardware | 3 | 2 | 01-Oct-14 A | 07-Oct-14 | 38 |
| L03-8128 | Install Shower/Tub Surrounds | 4 | 2 | 01-Oct-14 A | 07-Oct-14 | 25 |
| L04-8126 | Doors & Hardware | 3 | 2 | 02-Oct-14 A | 09-Oct-14 | 38 |
| L08-8116 | Install Base at Guestrooms | 5 | 3 | 02-Oct-14 A | 08-Oct-14 | 32 |
| L04-8110 | HVAC Trim / Finish (including Corridors) | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 58 |

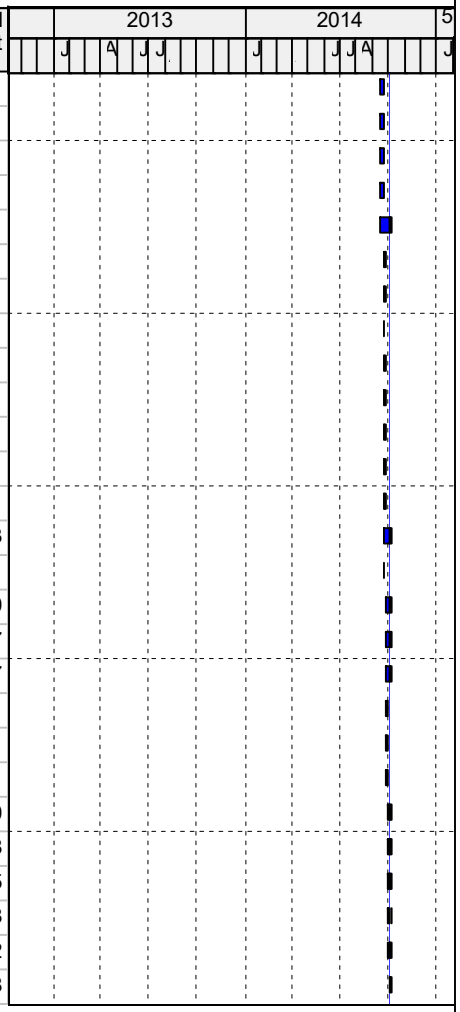



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8128 | Install Shower/Tub Surrounds | 4 | 4 | 06-Oct-14 | 09-Oct-14 | 25 |
| L05-8110 | HVAC Trim / Finish (including Corridors) | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 58 |
| L05-8120 | Install Countertops/Sills | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 17 |
| L05-8118 | Fire Alarm Trim / Finish | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 39 |
| L15-8105 | Paint (First Coat & Ceilings) | 3 | 3 | 06-Oct-14 | 08-Oct-14 | 23 |
| L16-8102S | Stock GWB | 1 | 1 | 06-Oct-14 | 06-Oct-14 | 15 |
| L16-8102 | Hang GWB & Inspection | 4 | 4 | 07-Oct-14 | 10-Oct-14 | 18 |
| L03-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 08-Oct-14 | 13-Oct-14 | 55 |
| L05-8128 | Install Shower/Tub Surrounds | 4 | 4 | 08-Oct-14 | 11-Oct-14 | 30 |
| L06-8110 | HVAC Trim / Finish (including Corridors) | 3 | 3 | 08-Oct-14 | 10-Oct-14 | 56 |
| L06-8118 | Fire Alarm Trim / Finish | 3 | 3 | 08-Oct-14 | 10-Oct-14 | 46 |
| L07-8110 | HVAC Trim / Finish (including Corridors) | 3 | 3 | 08-Oct-14 | 10-Oct-14 | 56 |
| L07-8118 | Fire Alarm Trim / Finish | 3 | 3 | 08-Oct-14 | 10-Oct-14 | 46 |
| L08-8108 | Elec Trim / Finish | 4 | 4 | 08-Oct-14 | 13-Oct-14 | 36 |
| L09-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 08-Oct-14 | 14-Oct-14 | 28 |
| L17-8102S | Stock GWB | 1 | 1 | 08-Oct-14 | 08-Oct-14 | 17 |
| L06-8120 | Install Countertops/Sills | 3 | 3 | 09-Oct-14 | 13-Oct-14 | 17 |
| L17-8102 | Hang GWB & Inspection | 4 | 4 | 09-Oct-14 | 13-Oct-14 | 20 |
| L04-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 10-Oct-14 | 15-Oct-14 | 53 |
| L06-8128 | Install Shower/Tub Surrounds | 4 | 4 | 10-Oct-14 | 15-Oct-14 | 25 |
| L08-8110 | HVAC Trim / Finish (including Corridors) | 3 | 3 | 10-Oct-14 | 14-Oct-14 | 54 |
| L08-8118 | Fire Alarm Trim / Finish | 3 | 3 | 10-Oct-14 | 14-Oct-14 | 47 |
| L09-8108 | Elec Trim / Finish | 4 | 4 | 10-Oct-14 | 15-Oct-14 | 34 |
| L09-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 10-Oct-14 | 15-Oct-14 | 34 |
| L09-8116 | Install Base at Guestrooms | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 28 |
| L10-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 10-Oct-14 | 16-Oct-14 | 28 |
| L05-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 13-Oct-14 | 16-Oct-14 | 52 |

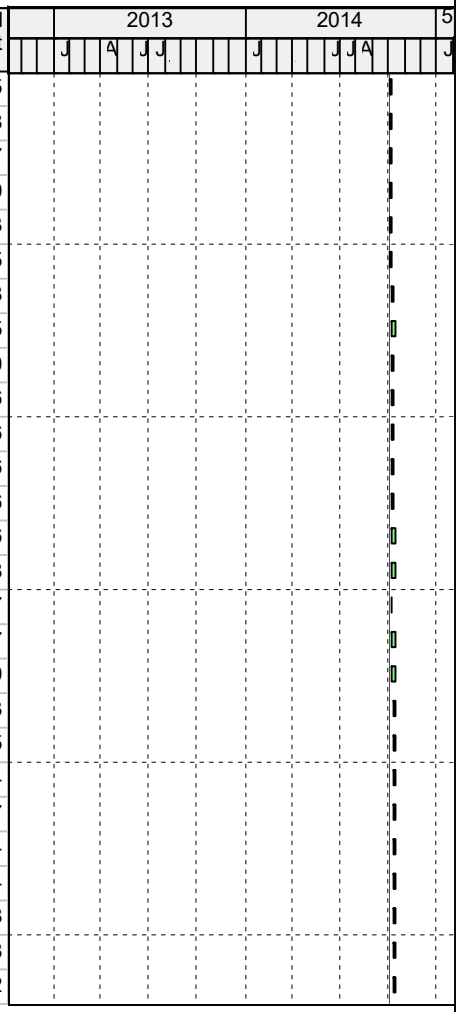


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8126 | Doors & Hardware | 3 | 3 | 13-Oct-14 | 15-Oct-14 | 35 |
| L10-8108 | Elec Trim / Finish | 4 | 4 | 13-Oct-14 | 16-Oct-14 | 23 |
| L11-8108 | Elec Trim / Finish | 4 | 4 | 13-Oct-14 | 16-Oct-14 | 33 |
| L11-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 13-Oct-14 | 16-Oct-14 | 33 |
| L03-8107 | Paint Final Coat | 3 | 3 | 14-Oct-14 | 16-Oct-14 | 47 |
| L03-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 48 |
| L07-8120 | Install Countertops/Sills | 3 | 3 | 14-Oct-14 | 16-Oct-14 | 17 |
| L07-8128 | Install Shower/Tub Surrounds | 4 | 4 | 14-Oct-14 | 17-Oct-14 | 25 |
| L09-8110 | HVAC Trim / Finish (including Corridors) | 3 | 3 | 14-Oct-14 | 16-Oct-14 | 52 |
| L10-8116 | Install Base at Guestrooms | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 28 |
| L11-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 14-Oct-14 | 20-Oct-14 | 28 |
| L12-8108 | Elec Trim / Finish | 4 | 4 | 14-Oct-14 | 17-Oct-14 | 32 |
| L12-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 14-Oct-14 | 17-Oct-14 | 32 |
| L04-8107 | Paint Final Coat | 4 | 4 | 15-Oct-14 | 20-Oct-14 | 41 |
| L04-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 15-Oct-14 | 16-Oct-14 | 43 |
| L10-8110 | HVAC Trim / Finish (including Corridors) | 3 | 3 | 15-Oct-14 | 17-Oct-14 | 51 |
| L10-8118 | Fire Alarm Trim / Finish | 3 | 3 | 15-Oct-14 | 17-Oct-14 | 46 |
| L11-8110 | HVAC Trim / Finish (including Corridors) | 3 | 3 | 15-Oct-14 | 17-Oct-14 | 51 |
| L11-8118 | Fire Alarm Trim / Finish | 3 | 3 | 15-Oct-14 | 17-Oct-14 | 46 |
| L05-8107 | Paint Final Coat | 3 | 3 | 16-Oct-14 | 20-Oct-14 | 32 |
| L05-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 32 |
| L06-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 16-Oct-14 | 21-Oct-14 | 49 |
| L06-8126 | Doors & Hardware | 3 | 3 | 16-Oct-14 | 18-Oct-14 | 34 |
| L08-8128 | Install Shower/Tub Surrounds | 4 | 4 | 16-Oct-14 | 21-Oct-14 | 25 |
| L11-8116 | Install Base at Guestrooms | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 28 |
| L12-8110 | HVAC Trim / Finish (including Corridors) | 3 | 3 | 16-Oct-14 | 20-Oct-14 | 50 |
| L12-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 16-Oct-14 | 22-Oct-14 | 28 |

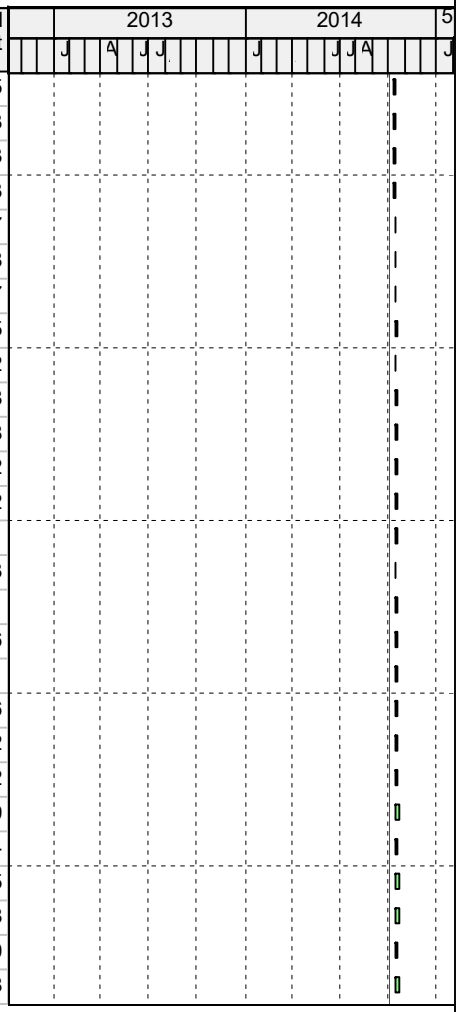



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8118 | Fire Alarm Trim / Finish | 3 | 3 | 16-Oct-14 | 20-Oct-14 | 46 |
| L14-8108 | Elec Trim / Finish | 4 | 4 | 16-Oct-14 | 21-Oct-14 | 30 |
| L14-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 16-Oct-14 | 21-Oct-14 | 30 |
| L16-8104 | Paint (Prime) | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 18 |
| L03-8114 | Signage (By Owner) | 5 | 5 | 17-Oct-14 | 23-Oct-14 | 52 |
| L08-8120 | Install Countertops/Sills | 3 | 3 | 17-Oct-14 | 21-Oct-14 | 17 |
| L07-8126 | Doors & Hardware | 3 | 3 | 18-Oct-14 | 21-Oct-14 | 34 |
| L07-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 20-Oct-14 | 23-Oct-14 | 47 |
| L09-8128 | Install Shower/Tub Surrounds | 4 | 4 | 20-Oct-14 | 23-Oct-14 | 25 |
| L12-8116 | Install Base at Guestrooms | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 28 |
| L14-8110 | HVAC Trim / Finish (including Corridors) | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 48 |
| L14-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 20-Oct-14 | 24-Oct-14 | 28 |
| L14-8118 | Fire Alarm Trim / Finish | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 44 |
| L15-8108 | Elec Trim / Finish | 4 | 4 | 20-Oct-14 | 23-Oct-14 | 28 |
| L15-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 20-Oct-14 | 23-Oct-14 | 28 |
| L16-8105 | Paint (First Coat & Ceilings) | 3 | 3 | 20-Oct-14 | 22-Oct-14 | 18 |
| L04-8114 | Signage (By Owner) | 5 | 5 | 21-Oct-14 | 27-Oct-14 | 50 |
| L05-8114 | Signage (By Owner) | 5 | 5 | 21-Oct-14 | 27-Oct-14 | 50 |
| L06-8107 | Paint Final Coat | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 39 |
| L06-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 22-Oct-14 | 23-Oct-14 | 40 |
| L08-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 22-Oct-14 | 27-Oct-14 | 45 |
| L08-8126 | Doors & Hardware | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 34 |
| L09-8120 | Install Countertops/Sills | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 17 |
| L10-8128 | Install Shower/Tub Surrounds | 4 | 4 | 22-Oct-14 | 27-Oct-14 | 25 |
| L14-8116 | Install Base at Guestrooms | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 28 |
| L15-8110 | HVAC Trim / Finish (including Corridors) | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 46 |
| L15-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 22-Oct-14 | 28-Oct-14 | 28 |

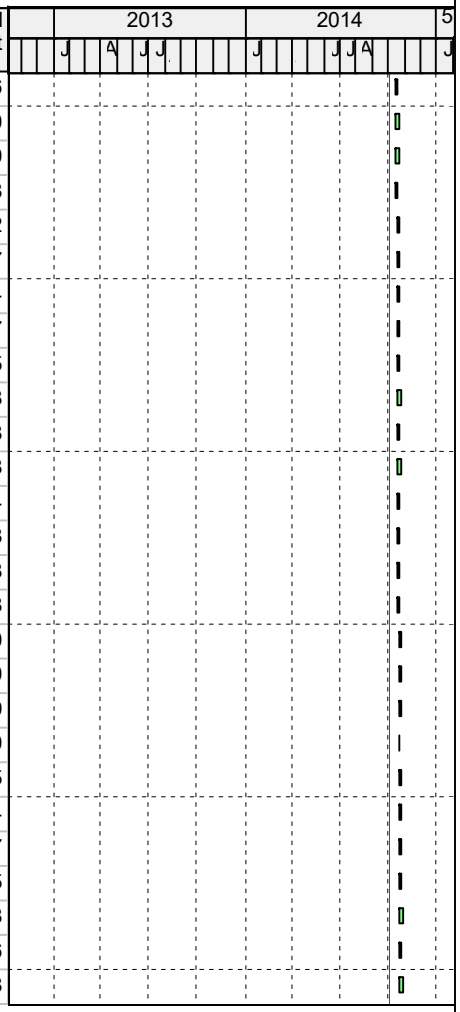



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8118 | Fire Alarm Trim / Finish | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 42 |
| L17-8104 | Paint (Prime) | 2 | 2 | 23-Oct-14 | 24-Oct-14 | 15 |
| L07-8107 | Paint Final Coat | 3 | 3 | 24-Oct-14 | 28-Oct-14 | 37 |
| L07-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 24-Oct-14 | 27-Oct-14 | 38 |
| L11-8128 | Install Shower/Tub Surrounds | 4 | 4 | 24-Oct-14 | 29-Oct-14 | 25 |
| L15-8116 | Install Base at Guestrooms | 5 | 5 | 24-Oct-14 | 30-Oct-14 | 28 |
| L09-8126 | Doors & Hardware | 3 | 3 | 25-Oct-14 | 28-Oct-14 | 33 |
| L06-8114 | Signage (By Owner) | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 46 |
| L09-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 27-Oct-14 | 30-Oct-14 | 42 |
| L10-8120 | Install Countertops/Sills | 3 | 3 | 27-Oct-14 | 29-Oct-14 | 17 |
| L17-8105 | Paint (First Coat & Ceilings) | 3 | 3 | 27-Oct-14 | 29-Oct-14 | 15 |
| L08-8107 | Paint Final Coat | 5 | 5 | 28-Oct-14 | 03-Nov-14 | 38 |
| L08-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 28-Oct-14 | 29-Oct-14 | 41 |
| L12-8128 | Install Shower/Tub Surrounds | 4 | 4 | 28-Oct-14 | 31-Oct-14 | 25 |
| L16-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 28-Oct-14 | 03-Nov-14 | 26 |
| L07-8114 | Signage (By Owner) | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 39 |
| L10-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 30-Oct-14 | 04-Nov-14 | 39 |
| L10-8126 | Doors & Hardware | 3 | 3 | 30-Oct-14 | 01-Nov-14 | 31 |
| L11-8120 | Install Countertops/Sills | 3 | 3 | 30-Oct-14 | 03-Nov-14 | 17 |
| L14-8128 | Install Shower/Tub Surrounds | 4 | 4 | 30-Oct-14 | 04-Nov-14 | 25 |
| L16-8108 | Elec Trim / Finish | 4 | 4 | 30-Oct-14 | 04-Nov-14 | 20 |
| L16-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 30-Oct-14 | 04-Nov-14 | 20 |
| L16-8116 | Install Base at Guestrooms | 5 | 5 | 30-Oct-14 | 05-Nov-14 | 26 |
| L09-8107 | Paint Final Coat | 3 | 3 | 31-Oct-14 | 04-Nov-14 | 38 |
| L09-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 31-Oct-14 | 03-Nov-14 | 39 |
| L04-8132 | Punchlist @ Guestrooms | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 41 |
| L04-8134 | Final Clean @ Guestrooms | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 41 |

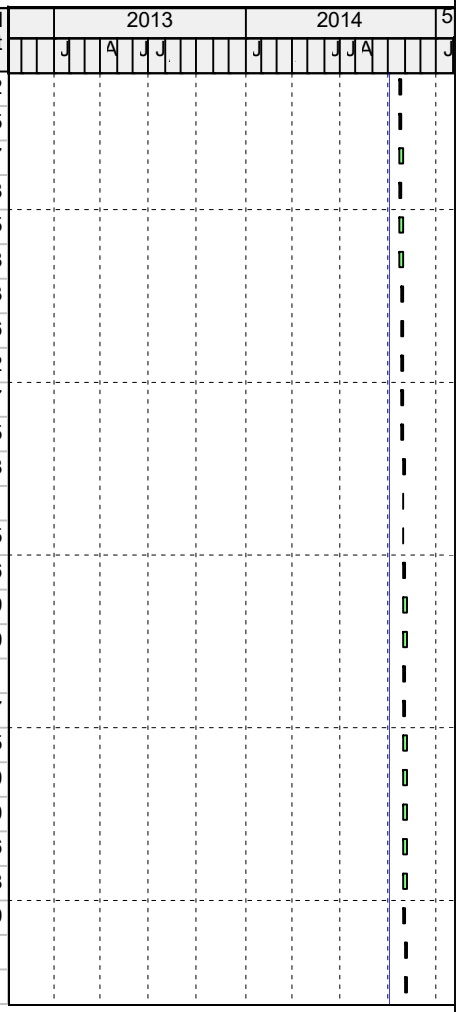



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8132 | Punchlist @ Guestrooms | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 41 |
| L05-8134 | Final Clean @ Guestrooms | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 41 |
| L15-8128 | Install Shower/Tub Surrounds | 4 | 4 | 03-Nov-14 | 06-Nov-14 | 25 |
| L16-8110 | HVAC Trim / Finish (including Corridors) | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 39 |
| L16-8118 | Fire Alarm Trim / Finish | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 32 |
| L08-8114 | Signage (By Owner) | 5 | 5 | 04-Nov-14 | 10-Nov-14 | 40 |
| L11-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 04-Nov-14 | 07-Nov-14 | 36 |
| L11-8126 | Doors & Hardware | 3 | 3 | 04-Nov-14 | 06-Nov-14 | 29 |
| L12-8120 | Install Countertops/Sills | 3 | 3 | 04-Nov-14 | 06-Nov-14 | 17 |
| L17-8124 | Guestroom/Bathroom Flooring | 5 | 5 | 04-Nov-14 | 10-Nov-14 | 24 |
| L06-8132 | Punchlist @ Guestrooms | 5 | 5 | 05-Nov-14 | 11-Nov-14 | 39 |
| L06-8134 | Final Clean @ Guestrooms | 5 | 5 | 05-Nov-14 | 11-Nov-14 | 39 |
| L09-8114 | Signage (By Owner) | 5 | 5 | 05-Nov-14 | 11-Nov-14 | 39 |
| L10-8107 | Paint Final Coat | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 34 |
| L10-8109 | Acoustical Ceiling Tile @ Corridors | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 34 |
| L16-8128 | Install Shower/Tub Surrounds | 4 | 4 | 05-Nov-14 | 10-Nov-14 | 25 |
| L08-8132 | Punchlist @ Guestrooms | 5 | 5 | 06-Nov-14 | 12-Nov-14 | 38 |
| L08-8134 | Final Clean @ Guestrooms | 5 | 5 | 06-Nov-14 | 12-Nov-14 | 38 |
| L17-8108 | Elec Trim / Finish | 4 | 4 | 06-Nov-14 | 11-Nov-14 | 15 |
| L17-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 06-Nov-14 | 11-Nov-14 | 15 |
| L17-8116 | Install Base at Guestrooms | 5 | 5 | 06-Nov-14 | 12-Nov-14 | 24 |
| L07-8132 | Punchlist @ Guestrooms | 5 | 5 | 07-Nov-14 | 13-Nov-14 | 37 |
| L07-8134 | Final Clean @ Guestrooms | 5 | 5 | 07-Nov-14 | 13-Nov-14 | 37 |
| L09-8132 | Punchlist @ Guestrooms | 5 | 5 | 07-Nov-14 | 13-Nov-14 | 37 |
| L09-8134 | Final Clean @ Guestrooms | 5 | 5 | 07-Nov-14 | 13-Nov-14 | 37 |
| L12-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 07-Nov-14 | 12-Nov-14 | 33 |
| L12-8126 | Doors & Hardware | 3 | 3 | 07-Nov-14 | 10-Nov-14 | 28 |

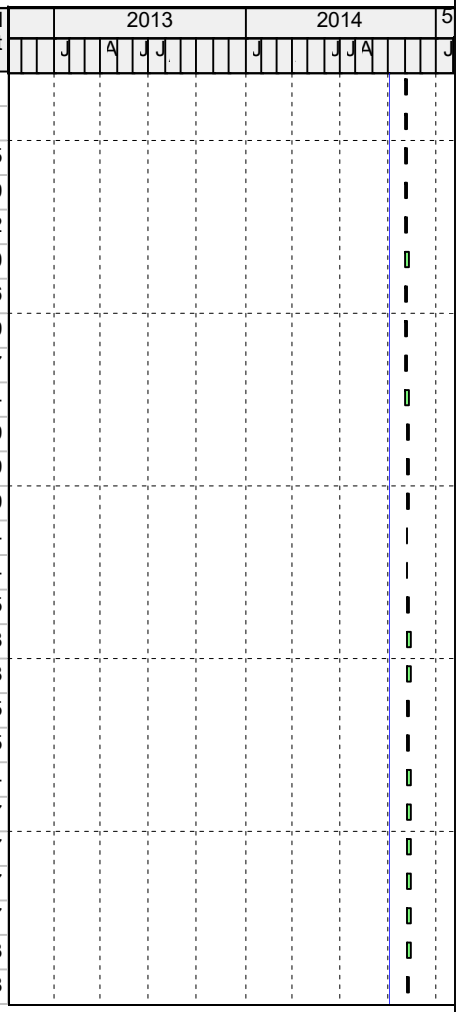



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8120 | Install Countertops/Sills | 3 | 3 | 07-Nov-14 | 11-Nov-14 | 17 |
| L17-8128 | Install Shower/Tub Surrounds | 4 | 4 | 07-Nov-14 | 12-Nov-14 | 25 |
| L10-8114 | Signage (By Owner) | 5 | 5 | 10-Nov-14 | 14-Nov-14 | 36 |
| L11-8107 | Paint Final Coat | 3 | 3 | 10-Nov-14 | 12-Nov-14 | 31 |
| L11-8109 | Acoustical Ceiling Tile @ Corridors | 3 | 3 | 10-Nov-14 | 12-Nov-14 | 31 |
| L17-8110 | HVAC Trim / Finish (including Corridors) | 3 | 3 | 10-Nov-14 | 12-Nov-14 | 33 |
| L17-8118 | Fire Alarm Trim / Finish | 3 | 3 | 10-Nov-14 | 12-Nov-14 | 29 |
| L10-8132 | Punchlist @ Guestrooms | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 34 |
| L10-8134 | Final Clean @ Guestrooms | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 34 |
| L14-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 12-Nov-14 | 17-Nov-14 | 30 |
| L14-8126 | Doors & Hardware | 3 | 3 | 12-Nov-14 | 14-Nov-14 | 26 |
| L15-8120 | Install Countertops/Sills | 3 | 3 | 12-Nov-14 | 14-Nov-14 | 17 |
| L11-8114 | Signage (By Owner) | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 33 |
| L12-8107 | Paint Final Coat | 3 | 3 | 13-Nov-14 | 17-Nov-14 | 29 |
| L12-8109 | Acoustical Ceiling Tile @ Corridors | 3 | 3 | 13-Nov-14 | 17-Nov-14 | 29 |
| L15-8126 | Doors & Hardware | 3 | 3 | 15-Nov-14 | 18-Nov-14 | 25 |
| L14-8107 | Paint Final Coat | 3 | 3 | 17-Nov-14 | 19-Nov-14 | 27 |
| L14-8109 | Acoustical Ceiling Tile @ Corridors | 3 | 3 | 17-Nov-14 | 19-Nov-14 | 27 |
| L15-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 17-Nov-14 | 20-Nov-14 | 27 |
| L16-8120 | Install Countertops/Sills | 3 | 3 | 17-Nov-14 | 19-Nov-14 | 17 |
| L11-8132 | Punchlist @ Guestrooms | 5 | 5 | 17-Nov-14 | 24-Nov-14 | 31 |
| L11-8134 | Final Clean @ Guestrooms | 5 | 5 | 17-Nov-14 | 24-Nov-14 | 31 |
| L12-8114 | Signage (By Owner) | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 30 |
| L12-8132 | Punchlist @ Guestrooms | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 28 |
| L12-8134 | Final Clean @ Guestrooms | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 28 |
| L14-8114 | Signage (By Owner) | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 28 |
| L16-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 20-Nov-14 | 25-Nov-14 | 25 |

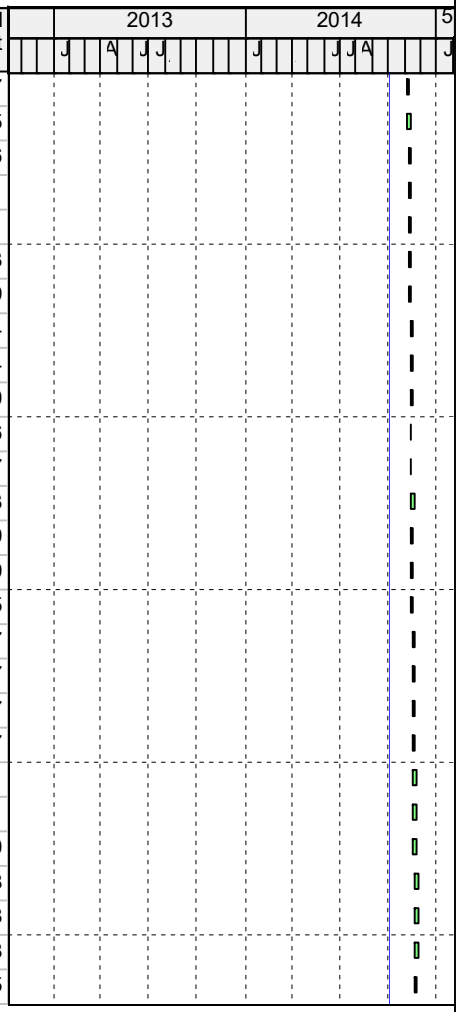



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8126 | Doors & Hardware | 3 | 3 | 20-Nov-14 | 22-Nov-14 | 23 |
| L17-8120 | Install Countertops/Sills | 3 | 3 | 20-Nov-14 | 24-Nov-14 | 17 |
| L15-8107 | Paint Final Coat | 3 | 3 | 21-Nov-14 | 25-Nov-14 | 23 |
| L15-8109 | Acoustical Ceiling Tile @ Corridors | 3 | 3 | 21-Nov-14 | 25-Nov-14 | 23 |
| L14-8132 | Punchlist @ Guestrooms | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 26 |
| L14-8134 | Final Clean @ Guestrooms | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 26 |
| L17-8122 | Plumbing Fixtures & Trim / Finish | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 21 |
| L17-8126 | Doors & Hardware | 3 | 3 | 25-Nov-14 | 01-Dec-14 | 23 |
| L15-8114 | Signage (By Owner) | 5 | 5 | 26-Nov-14 | 04-Dec-14 | 24 |
| L16-8107 | Paint Final Coat | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 18 |
| L16-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 19 |
| L15-8132 | Punchlist @ Guestrooms | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 22 |
| L15-8134 | Final Clean @ Guestrooms | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 22 |
| L03-8132 | Punchlist @ Guestrooms | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 21 |
| L03-8134 | Final Clean @ Guestrooms | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 21 |
| L16-8114 | Signage (By Owner) | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 21 |
| L17-8107 | Paint Final Coat | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 17 |
| L17-8109 | Acoustical Ceiling Tile @ Corridors | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 18 |
| L17-8114 | Signage (By Owner) | 5 | 5 | 08-Dec-14 | 12-Dec-14 | 18 |
| L16-8132 | Punchlist @ Guestrooms | 5 | 5 | 09-Dec-14 | 13-Dec-14 | 23 |
| L16-8134 | Final Clean @ Guestrooms | 5 | 5 | 09-Dec-14 | 13-Dec-14 | 23 |
| L17-8132 | Punchlist @ Guestrooms | 5 | 5 | 09-Dec-14 | 15-Dec-14 | 17 |
| L17-8134 | Final Clean @ Guestrooms | 5 | 5 | 09-Dec-14 | 15-Dec-14 | 17 |
| **Pool Area** | | | | | | |
| L03-8216 | Pool - Install tile, coping and depth markers | 10 | 10 | 24-Oct-14 | 06-Nov-14 | 9 |
| L03-8218 | Pool - Install pool equipment | 5 | 5 | 07-Nov-14 | 13-Nov-14 | 9 |
| **Corridors / Common / Public Areas** | | | | | | |

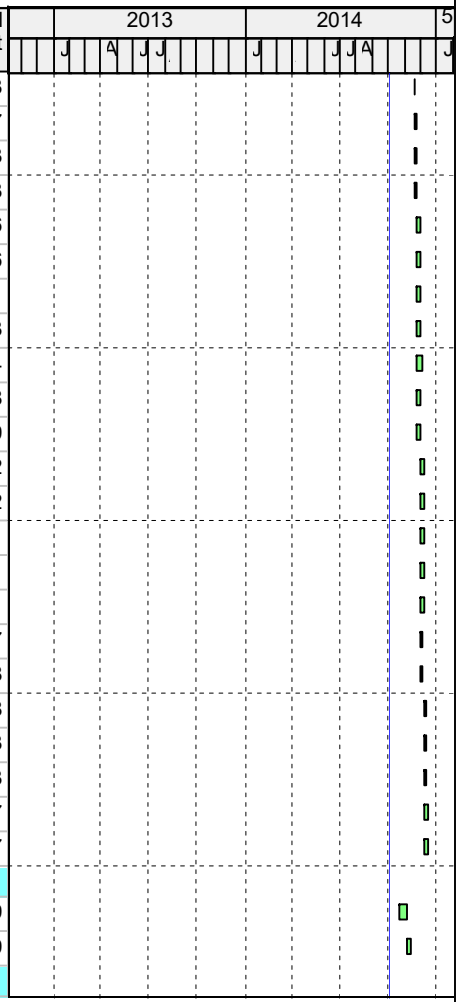



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8200 | Vinyl Wall Coverings | 3 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L04-8200 | Vinyl Wall Coverings | 5 | 0 | 06-Aug-14 A | 12-Aug-14 A | |
| L05-8200 | Vinyl Wall Coverings | 5 | 0 | 12-Aug-14 A | 22-Sep-14 A | |
| L03-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L06-8200 | Vinyl Wall Coverings | 5 | 2 | 10-Sep-14 A | 07-Oct-14 | 20 |
| L07-8200 | Vinyl Wall Coverings | 5 | 2 | 10-Sep-14 A | 07-Oct-14 | 23 |
| L08-8200 | Vinyl Wall Coverings | 5 | 2 | 11-Sep-14 A | 07-Oct-14 | 21 |
| L04-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| L05-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L06-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L07-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L09-8200 | Vinyl Wall Coverings | 5 | 3 | 29-Sep-14 A | 09-Oct-14 | 21 |
| L10-8200 | Vinyl Wall Coverings | 5 | 4 | 29-Sep-14 A | 10-Oct-14 | 21 |
| L11-8200 | Vinyl Wall Coverings | 5 | 4 | 29-Sep-14 A | 10-Oct-14 | 21 |
| L12-8200 | Vinyl Wall Coverings | 5 | 5 | 07-Oct-14 | 13-Oct-14 | 21 |
| L14-8200 | Vinyl Wall Coverings | 5 | 5 | 09-Oct-14 | 15-Oct-14 | 21 |
| L08-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 10-Oct-14 | 13-Oct-14 | 51 |
| L15-8200 | Vinyl Wall Coverings | 5 | 5 | 13-Oct-14 | 17-Oct-14 | 21 |
| L09-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 14-Oct-14 | 15-Oct-14 | 50 |
| L10-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 15-Oct-14 | 16-Oct-14 | 47 |
| L11-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 15-Oct-14 | 16-Oct-14 | 47 |
| L12-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 16-Oct-14 | 17-Oct-14 | 47 |
| L14-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 20-Oct-14 | 21-Oct-14 | 45 |
| L04-8206 | Install Flooring @ Corridors | 2 | 2 | 21-Oct-14 | 22-Oct-14 | 41 |
| L05-8206 | Install Flooring @ Corridors | 5 | 5 | 21-Oct-14 | 27-Oct-14 | 44 |
| L15-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 22-Oct-14 | 23-Oct-14 | 43 |
| L16-8200 | Vinyl Wall Coverings | 5 | 5 | 23-Oct-14 | 29-Oct-14 | 18 |

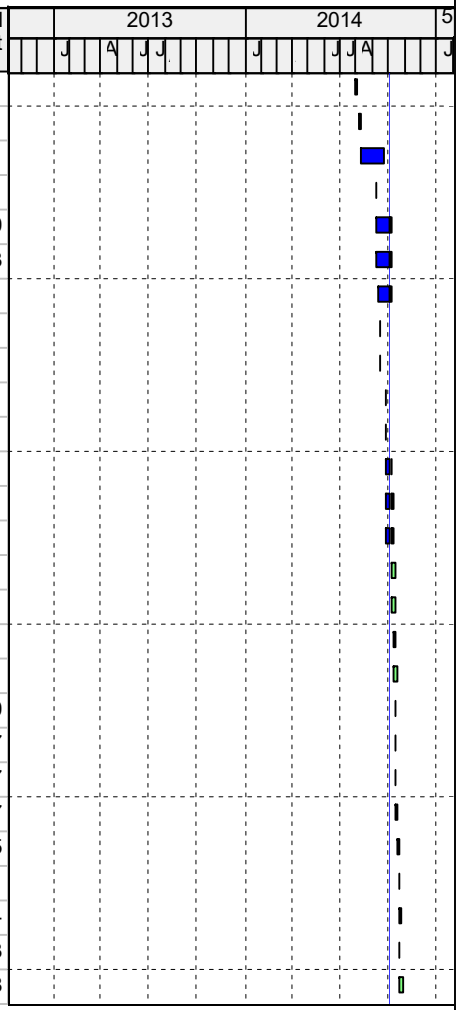



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8206 | Install Flooring @ Corridors | 5 | 5 | 27-Oct-14 | 31-Oct-14 | 39 |
| L07-8206 | Install Flooring @ Corridors | 5 | 5 | 29-Oct-14 | 04-Nov-14 | 37 |
| L17-8200 | Vinyl Wall Coverings | 5 | 5 | 30-Oct-14 | 05-Nov-14 | 15 |
| L16-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 34 |
| L08-8206 | Install Flooring @ Corridors | 2 | 2 | 04-Nov-14 | 05-Nov-14 | 38 |
| L09-8206 | Install Flooring @ Corridors | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 38 |
| L04-8208 | Final Clean (Entire Floor) | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 41 |
| L05-8208 | Final Clean (Entire Floor) | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 41 |
| L10-8206 | Install Flooring @ Corridors | 3 | 3 | 10-Nov-14 | 12-Nov-14 | 34 |
| L17-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 31 |
| L04-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 12-Nov-14 | 12-Nov-14 | 41 |
| L05-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 12-Nov-14 | 12-Nov-14 | 41 |
| L06-8208 | Final Clean (Entire Floor) | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 39 |
| L04-8212 | Resolve Final Punchlist | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 41 |
| L05-8212 | Resolve Final Punchlist | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 41 |
| L08-8208 | Final Clean (Entire Floor) | 2 | 2 | 13-Nov-14 | 14-Nov-14 | 38 |
| L11-8206 | Install Flooring @ Corridors | 3 | 3 | 13-Nov-14 | 17-Nov-14 | 31 |
| L06-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 14-Nov-14 | 14-Nov-14 | 39 |
| L07-8208 | Final Clean (Entire Floor) | 2 | 2 | 14-Nov-14 | 17-Nov-14 | 37 |
| L09-8208 | Final Clean (Entire Floor) | 2 | 2 | 14-Nov-14 | 17-Nov-14 | 37 |
| L06-8212 | Resolve Final Punchlist | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 39 |
| L08-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 17-Nov-14 | 17-Nov-14 | 38 |
| L07-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 18-Nov-14 | 18-Nov-14 | 37 |
| L08-8212 | Resolve Final Punchlist | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 38 |
| L09-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 18-Nov-14 | 18-Nov-14 | 37 |
| L12-8206 | Install Flooring @ Corridors | 4 | 4 | 18-Nov-14 | 21-Nov-14 | 35 |
| L07-8212 | Resolve Final Punchlist | 5 | 5 | 19-Nov-14 | 25-Nov-14 | 37 |

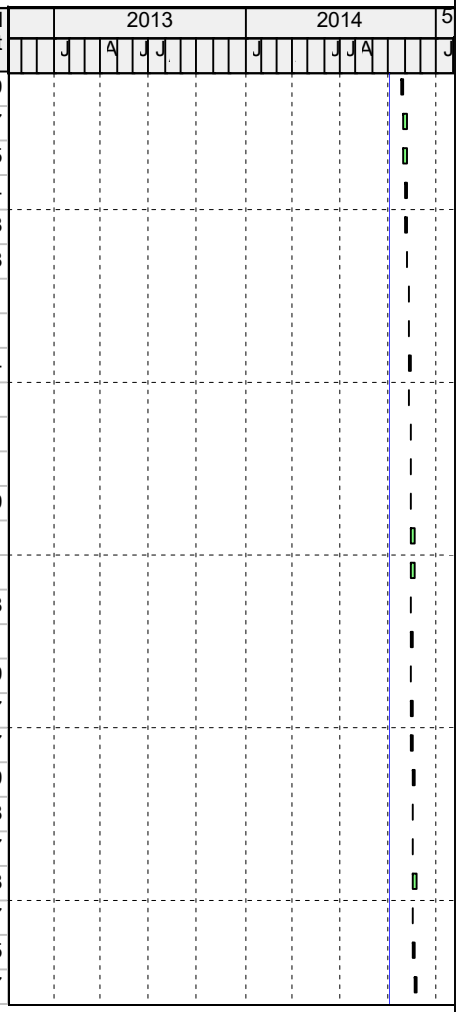


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8212 | Resolve Final Punchlist | 5 | 5 | 19-Nov-14 | 25-Nov-14 | 37 |
| L10-8208 | Final Clean (Entire Floor) | 2 | 2 | 19-Nov-14 | 20-Nov-14 | 34 |
| L04-8214 | Floor Complete | 0 | 0 | | 19-Nov-14 | 41 |
| L05-8214 | Floor Complete | 0 | 0 | | 19-Nov-14 | 41 |
| L14-8206 | Install Flooring @ Corridors | 4 | 4 | 20-Nov-14 | 24-Nov-14 | 33 |
| L03-8206 | Install Flooring @ Corridors | 4 | 4 | 21-Nov-14 | 25-Nov-14 | 26 |
| L10-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 21-Nov-14 | 21-Nov-14 | 34 |
| L06-8214 | Floor Complete | 0 | 0 | | 21-Nov-14 | 39 |
| L10-8212 | Resolve Final Punchlist | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 34 |
| L11-8208 | Final Clean (Entire Floor) | 2 | 2 | 24-Nov-14 | 26-Nov-14 | 31 |
| L08-8214 | Floor Complete | 0 | 0 | | 24-Nov-14 | 38 |
| L07-8214 | Floor Complete | 0 | 0 | | 25-Nov-14 | 37 |
| L09-8214 | Floor Complete | 0 | 0 | | 25-Nov-14 | 37 |
| L15-8206 | Install Flooring @ Corridors | 4 | 4 | 26-Nov-14 | 03-Dec-14 | 28 |
| L11-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 26-Nov-14 | 01-Dec-14 | 31 |
| L12-8208 | Final Clean (Entire Floor) | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 28 |
| L11-8212 | Resolve Final Punchlist | 5 | 5 | 01-Dec-14 | 08-Dec-14 | 31 |
| L10-8214 | Floor Complete | 0 | 0 | | 02-Dec-14 | 34 |
| L12-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 28 |
| L14-8208 | Final Clean (Entire Floor) | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 26 |
| L16-8206 | Install Flooring @ Corridors | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 18 |
| L12-8212 | Resolve Final Punchlist | 5 | 5 | 04-Dec-14 | 10-Dec-14 | 28 |
| L14-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 05-Dec-14 | 05-Dec-14 | 26 |
| L17-8206 | Install Flooring @ Corridors | 4 | 4 | 06-Dec-14 | 10-Dec-14 | 22 |
| L14-8212 | Resolve Final Punchlist | 5 | 5 | 08-Dec-14 | 12-Dec-14 | 26 |
| L11-8214 | Floor Complete | 0 | 0 | | 08-Dec-14 | 31 |
| L15-8208 | Final Clean (Entire Floor) | 2 | 2 | 09-Dec-14 | 10-Dec-14 | 22 |

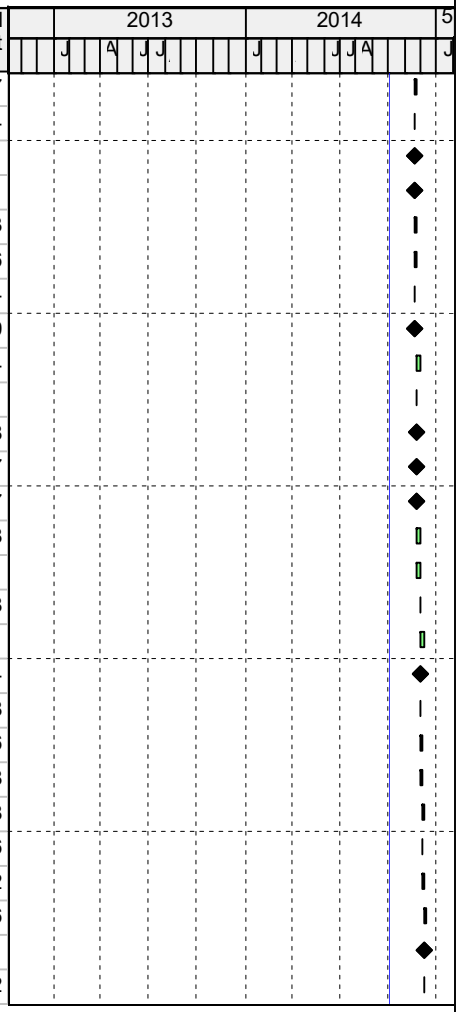


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8214 | Floor Complete | 0 | 0 | | 10-Dec-14 | 28 |
| L15-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 11-Dec-14 | 11-Dec-14 | 22 |
| L15-8212 | Resolve Final Punchlist | 5 | 5 | 12-Dec-14 | 18-Dec-14 | 22 |
| L14-8214 | Floor Complete | 0 | 0 | | 12-Dec-14 | 26 |
| L16-8208 | Final Clean (Entire Floor) | 2 | 2 | 15-Dec-14 | 16-Dec-14 | 18 |
| L17-8208 | Final Clean (Entire Floor) | 2 | 2 | 16-Dec-14 | 17-Dec-14 | 17 |
| L16-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 17-Dec-14 | 17-Dec-14 | 18 |
| L16-8212 | Resolve Final Punchlist | 5 | 5 | 18-Dec-14 | 24-Dec-14 | 18 |
| L17-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 18-Dec-14 | 18-Dec-14 | 17 |
| L15-8214 | Floor Complete | 0 | 0 | | 18-Dec-14 | 22 |
| L17-8212 | Resolve Final Punchlist | 5 | 5 | 19-Dec-14 | 29-Dec-14 | 17 |
| L16-8214 | Floor Complete | 0 | 0 | | 24-Dec-14 | 18 |
| L17-8214 | Floor Complete | 0 | 0 | | 29-Dec-14 | 17 |
| L03-8208 | Final Clean (Entire Floor) | 2 | 2 | 30-Dec-14 | 31-Dec-14 | 9 |
| L03-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 02-Jan-15 | 02-Jan-15 | 9 |
| L03-8212 | Resolve Final Punchlist | 5 | 5 | 05-Jan-15 | 09-Jan-15 | 9 |
| L03-8214 | Floor Complete | 0 | 0 | | 09-Jan-15 | 9 |
| **Mech Penthouse** | | | | | | |
| PH-8102 | PH - Complete GWB Hang / Tape / Finish | 4 | 4 | 22-Oct-14 | 27-Oct-14 | 24 |
| PH-8100 | PH - Insulation | 3 | 3 | 22-Oct-14 | 24-Oct-14 | 24 |
| PH-8104 | PH - Int Painting | 5 | 5 | 28-Oct-14 | 03-Nov-14 | 24 |
| PH-8122 | PH - Plumbing Trim / Finish | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 24 |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 2 | 2 | 04-Nov-14 | 05-Nov-14 | 29 |
| PH-8114 | PH - Signage | 2 | 2 | 04-Nov-14 | 05-Nov-14 | 42 |
| PH-8108 | PH - Elec Trim / Finish | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 24 |
| PH-8110 | PH - HVAC Trim / Finish | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 28 |
| PH-8118 | PH - Elec Specialties Trim / Finish | 3 | 3 | 10-Nov-14 | 12-Nov-14 | 24 |

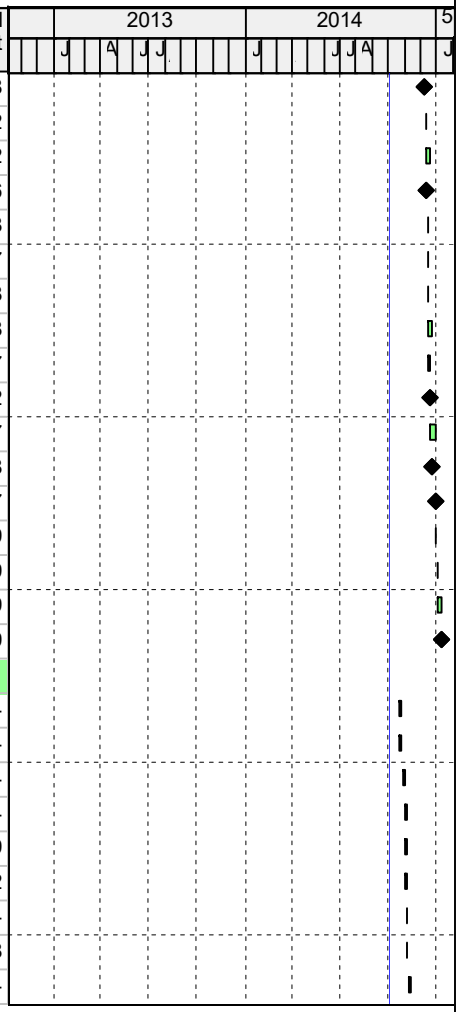



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-8124 | PH - Flooring | 4 | 4 | 13-Nov-14 | 18-Nov-14 | 24 |
| PH-8126 | PH - Doors & Hardware | 3 | 3 | 17-Nov-14 | 19-Nov-14 | 24 |
| PH-8134 | PH - Pre-Clean | 3 | 3 | 20-Nov-14 | 24-Nov-14 | 24 |
| PH-8132 | PH - Contractor Pre-Punchlist | 5 | 5 | 25-Nov-14 | 03-Dec-14 | 24 |
| PH-8208 | PH - Final Clean | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 24 |
| PH-8210 | PH - Owner Walk / Create Punchlist | 1 | 1 | 09-Dec-14 | 09-Dec-14 | 24 |
| PH-8212 | PH - Final Punchlist | 5 | 5 | 10-Dec-14 | 16-Dec-14 | 24 |
| PH-8214 | PH - Floor Complete | 0 | 0 | | 16-Dec-14 | 24 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| **Smoke Control** | | | | | | |
| CO-7104 | Smoke Control Pre-Testing (Podium) | 12 | 12 | 22-Dec-14 | 09-Jan-15 | 4 |
| CO-7106 | City of Bellevue Smoke Control Testing (Podium) | 5 | 5 | 12-Jan-15 | 16-Jan-15 | 4 |
| CO-7108 | Final Marriott Smoke Control Testing | 5 | 5 | 19-Jan-15 | 23-Jan-15 | 4 |
| **Fire Sprinklers** | | | | | | |
| CO-7110 | Fire Sprinkler Pre-Testing (Podium) | 12 | 12 | 22-Dec-14 | 09-Jan-15 | 4 |
| CO-7112 | City of Bellevue Fire Sprinkler Inspection / Approval (F | 5 | 5 | 12-Jan-15 | 16-Jan-15 | 4 |
| CO-7114 | Marriott Fire Sprinkler Testing | 5 | 5 | 19-Jan-15 | 23-Jan-15 | 4 |
| **Fire Alarm** | | | | | | |
| CO-7116 | Fire Alarm Pre-Testing (Podium) | 12 | 12 | 22-Dec-14 | 09-Jan-15 | 4 |
| CO-7118 | City of Bellevue Fire Alarm Inspection / Approval (Pod | 5 | 5 | 12-Jan-15 | 16-Jan-15 | 4 |
| CO-7120 | Marriott Fire Alarm Testing | 5 | 5 | 19-Jan-15 | 23-Jan-15 | 4 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| CO-7100 | Cx - Equipment Start-Up & Testing, Podium | 15 | 15 | 10-Nov-14 | 02-Dec-14 | 17 |
| CO-7102 | Cx - DDC Point-To-Point Checks, Podium | 10 | 10 | 17-Nov-14 | 02-Dec-14 | 34 |

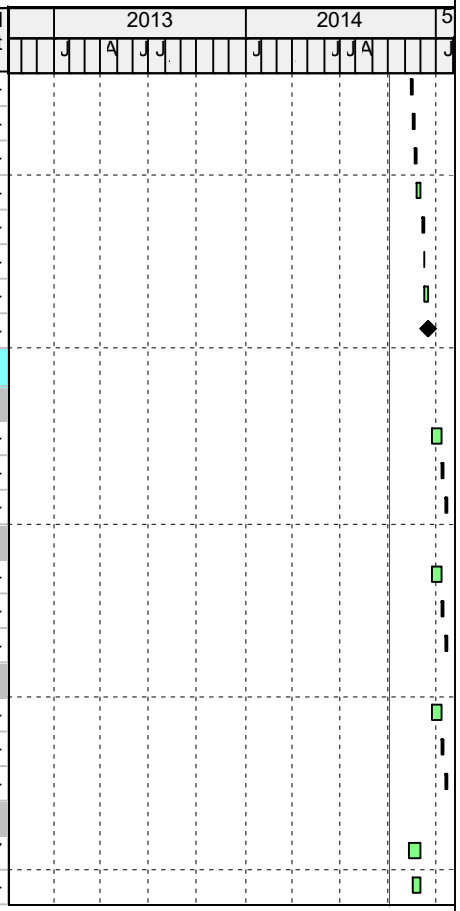



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Working Schedule - 11-2-14 Update** | | | | | | |
| L09-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-04 A | 30-Sep-14 A | |
| I-1500 | Owner release revised LV design - Tower (ASIs 5, 13, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-1550 | Owner release revised LV design - Podium (ASIs 5, 1 | 200 | 0 | 23-May-13 A | 28-Apr-14 A | |
| I-1900 | Owner issue design revisions (ASIs 4, 9, 19, 34) | 215 | 0 | 23-May-13 A | 24-Mar-14 A | |
| I-2500 | Owner issue LL1 electrical revisions (ASIs 7, 9r2, 14, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-3400 | Owner provide Level 2 ceiling heights | 180 | 0 | 24-Jun-13 A | 24-Mar-14 A | |
| I-3700 | Owner resolve wall condition between stair and Eleva | 200 | 0 | 27-Jun-13 A | 16-Jun-14 A | |
| MM-1000 | MM - Temporary Power Available | 0 | 0 | 08-Jul-13 A | | |
| I-2100 | Owner revise roof steel design (Submittals 365, 370, | 200 | 0 | 09-Jul-13 A | 07-Apr-14 A | |
| I-2200 | Owner resolve elevator steel issue (RFI 112, RFI 112. | 200 | 0 | 09-Jul-13 A | 03-Mar-14 A | |
| I-2400 | Owner provide Tower light fixture selections (ASI 36) | 185 | 0 | 18-Jul-13 A | 08-Apr-14 A | |
| I-2900 | Owner revise Food Service and Kitchen (ASIs 11, 12, | 140 | 0 | 08-Aug-13 A | 27-Feb-14 A | |
| I-1400 | Owner develop envelope redesign | 70 | 0 | 27-Aug-13 A | 12-Dec-13 A | |
| I-3600 | Owner closeout glass/glazing allowance | 160 | 0 | 04-Sep-13 A | 30-Apr-14 A | |
| I-1200 | Owner release revised Concierge Lounge design (AS | 160 | 0 | 06-Sep-13 A | 08-Apr-14 A | |
| I-2800 | Owner revise interior public space design (ASIs 16, 18 | 130 | 0 | 25-Sep-13 A | 09-Apr-14 A | |
| I-2000 | Owner approve door frames (Submittals 258, 454, 48 | 85 | 0 | 27-Sep-13 A | 23-Jan-14 A | |
| I-3100 | Owner revise ballroom ceiling design (ASIs 18, 25) | 100 | 0 | 17-Oct-13 A | 25-Feb-14 A | |
| I-1600 | Owner provide directive for south & east corridor encl | 110 | 0 | 28-Oct-13 A | 18-Apr-14 A | |
| I-2300 | Owner resolve fire smoke dampers issue (RFI 233) | 115 | 0 | 30-Oct-13 A | 11-Apr-14 A | |
| I-2600 | Owner resolve L2 slab coordination issue | 4 | 0 | 13-Nov-13 A | 16-Nov-13 A | |
| I-2700 | Owner revise tower guest rooms design (ASIs 23, 29) | 58 | 0 | 04-Dec-13 A | 26-Feb-14 A | |
| I-1700 | Owner provide design for dry site utilities (ASIs 20, 20 | 66 | 0 | 09-Dec-13 A | 13-Mar-14 A | |
| I-1402 | Begin exterior panel production | 41 | 0 | 13-Dec-13 A | 12-Feb-14 A | |
| I-1300 | Owner issue "Hold" directive (email) | 0 | 0 | | 19-Dec-13 A | |
| I-1100 | Owner release revised L17 design (ASI 23, 29R1) | 74 | 0 | 20-Dec-13 A | 08-Apr-14 A | |

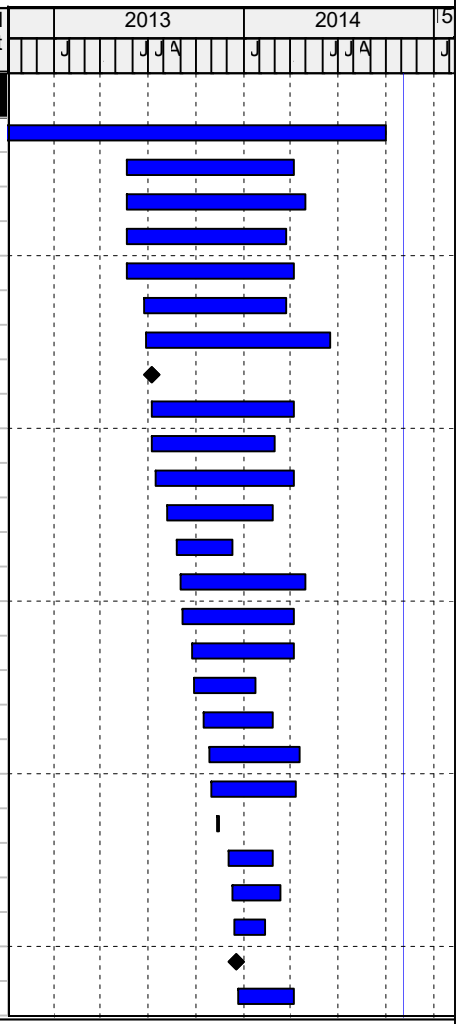


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1302 | Owner issue ASI 30 (Prep Kitchen Revisions) | 47 | 0 | 20-Dec-13 A | 27-Feb-14 A | |
| I-1404 | City of Bellevue Approval | 90 | 0 | 23-Dec-13 A | 15-Jul-14 A | |
| I-3000 | Owner revise bar area (change to straight bar, IDRFI-( | 71 | 0 | 22-Jan-14 A | 27-May-14 A | |
| I-1306 | Prep Kitchen - Additional plumbing (ASI 30) | 4 | 0 | 17-Feb-14 A | 01-Aug-14 A | |
| I-2202 | Fabricate revised elevator steel | 60 | 0 | 04-Mar-14 A | 07-May-14 A | |
| I-2704 | Framing "Go Back" work for ASIs 23, 29 - L4 | 1 | 0 | 05-Mar-14 A | 12-Mar-14 A | |
| I-3900 | RFI 471, Resolve Ballroom parapet height issue | 1 | 0 | 08-Mar-14 A | 07-May-14 A | |
| I-1702 | Owner provide directive to proceed | 26 | 0 | 14-Mar-14 A | 01-May-14 A | |
| I-3300 | Owner provide Guest Room plumbing fixture selectio | 1 | 0 | 20-Mar-14 A | 20-Mar-14 A | |
| I-1902 | Procure revised structural steel | 15 | 0 | 25-Mar-14 A | 14-Apr-14 A | |
| I-4000 | Owner complete design of east stitched enclosure (fo | 1 | 0 | 01-Apr-14 A | 14-May-14 A | |
| I-2102 | Fabricate revised roof steel | 20 | 0 | 08-Apr-14 A | 15-May-14 A | |
| I-3200 | Owner provide light fixture selections for podium level | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| I-3800 | Resolve Heat Pump Electrical Overcurrent Issue | 20 | 0 | 23-Apr-14 A | 18-Jun-14 A | |
| L10-8221 | HVAC Risers Duct Insulation | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L11-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| I-2304 | Framing "Go Back" work at L3 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2306 | Framing "Go Back" work at L4 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2308 | Framing "Go Back" work at L5 for RFI 233 | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2706 | Framing "Go Back" work for ASIs 23, 29 - L5 | 1 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2708 | Framing "Go Back" work for ASIs 23, 29 - L6 | 1 | 0 | 29-Apr-14 A | 09-May-14 A | |
| I-2702 | Framing "Go Back" work for ASIs 23, 29 - L3 | 1 | 0 | 01-May-14 A | 01-May-14 A | |
| I-1706 | PSE scheduling delay | 10 | 0 | 01-May-14 A | 20-May-14 A | |
| I-3602 | Complete shop drawings & fab/deliver storefront fram | 40 | 0 | 01-May-14 A | 14-Jun-14 A | |
| L04-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| I-1802 | Rework framing for door hold-opens - LL4 | 1 | 0 | 07-May-14 A | 08-May-14 A | |

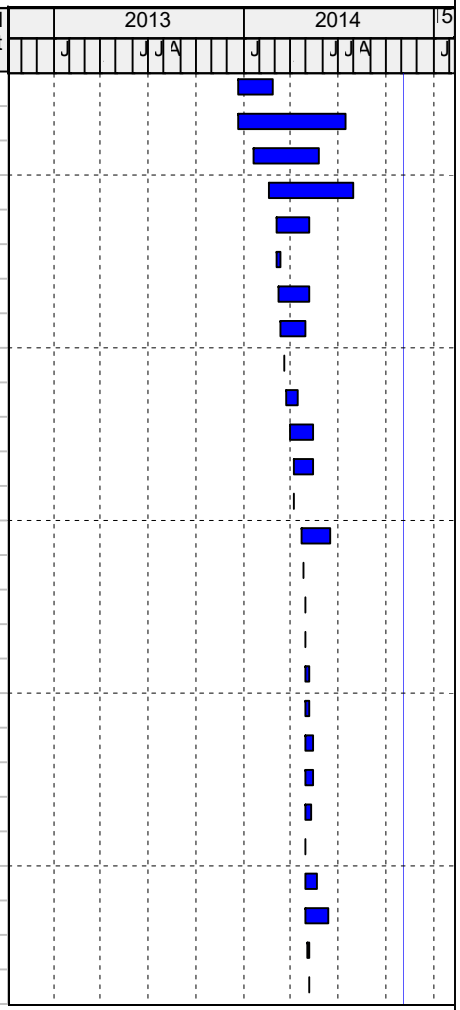



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-May-14 A | 12-May-14 A | |
| I-1800 | Owner issue directive to proceed with door hold-open | 1 | 0 | 08-May-14 A | 08-May-14 A | |
| I-1804 | Rework framing for door hold-opens - LL3 | 1 | 0 | 08-May-14 A | 09-May-14 A | |
| I-2312 | Framing "Go Back" work at L7 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-2314 | Framing "Go Back" work at L8 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-3902 | Install Ballroom parapet extension | 5 | 0 | 08-May-14 A | 13-May-14 A | |
| I-1806 | Rework framing for door hold-opens - LL2 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-1808 | Rework framing for door hold-opens - LL1 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-2310 | Framing "Go Back" work at L6 for RFI 233 | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| I-2710 | Framing "Go Back" work for ASIs 23, 29 - L7 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| L05-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L06-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L05-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| LL2E-8110 | LL2 - Electrical, Fire pumps/equipment final connectic | 5 | 0 | 12-May-14 A | 30-Oct-14 A | |
| PH-8704 | PH - Install Machine Support Steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| PH-8710 | Install elevator rail support steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| L03-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L03-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 13-May-14 A | 14-May-14 A | |
| I-4002 | East Stitched - Install framing and windows | 9 | 0 | 19-May-14 A | 09-Jun-14 A | |
| L10-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L11-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L12-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| RF-4038 | AR - Concrete pads and curbs | 5 | 0 | 21-May-14 A | 04-Jun-14 A | |
| L10-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L11-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L12-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |

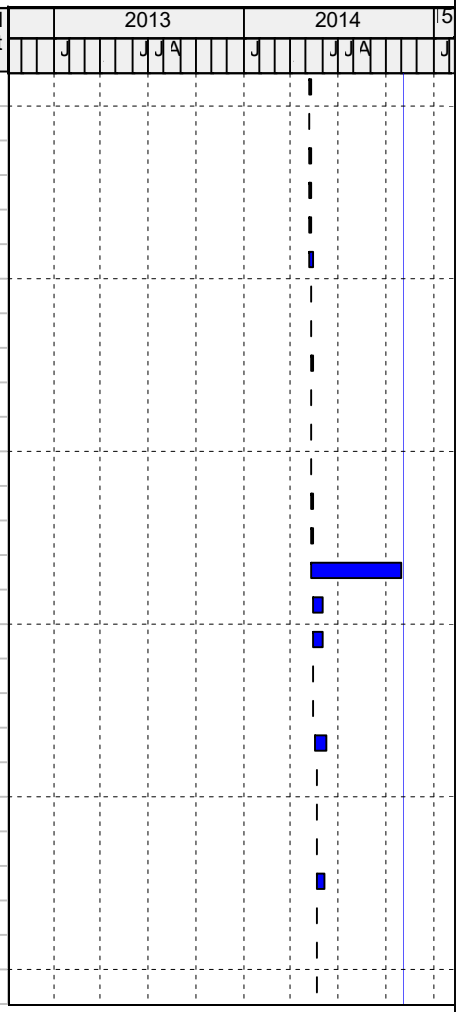



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L15-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 27-May-14 A | |
| L11-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 07-Jun-14 A | |
| L12-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 27-May-14 A | 06-Jun-14 A | |
| I-3002 | City of Bellevue approve bar design changes. | 5 | 2 | 28-May-14 A | 04-Nov-14 | 6 |
| L16-8221 | HVAC Risers Duct Insulation | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| PH-8712 | PH - Complete Framing and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| PH-8714 | Stage PH/L18 roofing materials | 2 | 0 | 30-May-14 A | 30-May-14 A | |
| L08-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L08-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 02-Jun-14 A | 20-Jun-14 A | |
| PH-8704I | Correct support steel embeds | 2 | 0 | 02-Jun-14 A | 11-Jun-14 A | |
| L14-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 03-Jun-14 A | 04-Jun-14 A | |
| L17-8221 | HVAC Risers Duct Insulation | 1 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| PC-4010 | PC - Fireproof Entry Roof Steel | 5 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| I-4100 | Owner resolve trap primers issue (RFI 560) | 5 | 0 | 03-Jun-14 A | 20-Jun-14 A | |
| RF-6028 | Tower Roof - Structural Steel | 5 | 0 | 04-Jun-14 A | 17-Jun-14 A | |
| L14-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L1B-6005 | Head of Wall Fire Caulk at CMU (including East Servi | 2 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L14-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L15-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |

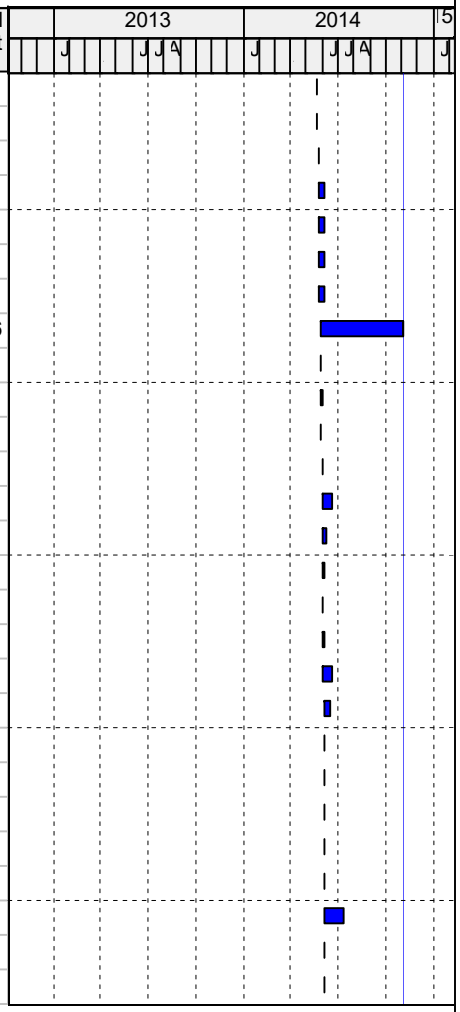



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L09-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 11-Jun-14 A | 12-Jun-14 A | |
| I-3702 | Complete wall framing at Stair/Elevator 5 (LL4) | 2 | 0 | 18-Jun-14 A | 20-Jun-14 A | |
| I-3720 | Fireproof added steel between Stair 1 and Elevator 5 | 5 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| I-3722 | Complete GWB between Stair 1 and Elevator 5 shaft | 10 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| LL1-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 22-Jul-14 A | |
| TC-5912 | Tower Crane pour-backs (LL4 to L3) | 4 | 0 | 19-Jun-14 A | 26-Jun-14 A | |
| LL1-Z2-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL4-6005 | LL4 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| LL3-6005 | LL3 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| L03-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 21-Jun-14 A | 21-Jun-14 A | |
| L06-6040 | Test Heat Pumps - L3, L4, L5 and L6 | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L03-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| L17-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL2-6005 | LL2 - Seismic Head Of Wall Fire Caulk at CMU | 5 | 0 | 24-Jun-14 A | 18-Jul-14 A | |
| I-3704 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL1-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z2-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z3-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 04-Aug-14 A | |
| L1L-6005 | Head of Wall Fire Caulk at CMU (including back of ho | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1K-6005 | Head of Wall Fire Caulk at CMU & Inspection | 2 | 0 | 24-Jun-14 A | 08-Aug-14 A | |
| L03-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L04-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| I-3710 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| I-3712 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| L1K-6018a | Install Kitchen hoods and grease ducts (OFCI) | 10 | 0 | 25-Jun-14 A | 07-Oct-14 A | |

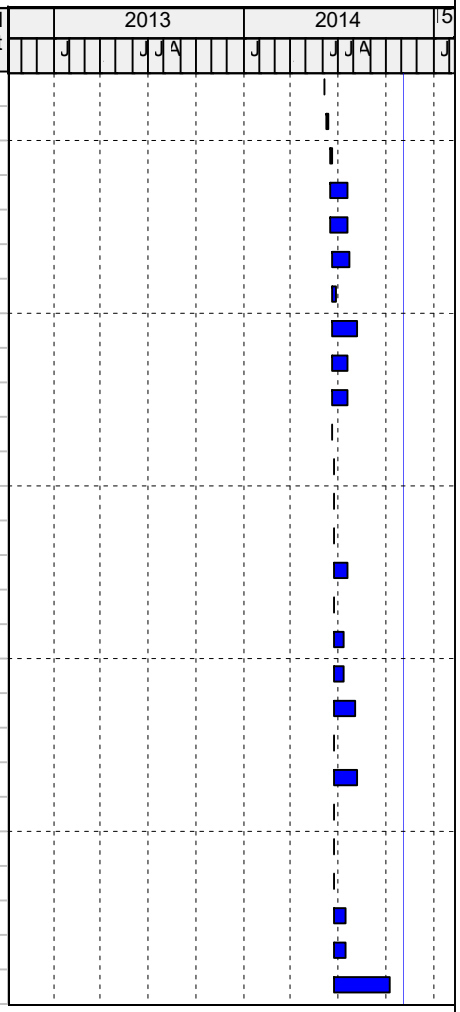


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8604 | L3 Pool - Plumbing R/I | 5 | 1 | 25-Jun-14 A | 25-Nov-14 | 16 |
| L04-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 26-Jun-14 A | 03-Jul-14 A | |
| L09-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 26-Jun-14 A | 26-Jun-14 A | |
| I-3706 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 26-Jun-14 A | 10-Jul-14 A | |
| L03-8600 | L3 Pool - Framing & HM frames | 5 | 1 | 26-Jun-14 A | 24-Nov-14 | 16 |
| L05-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L08-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L04-7018 | Electrical Rough-In | 1 | 0 | 27-Jun-14 A | 22-Jul-14 A | |
| L04-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 27-Jun-14 A | 23-Jul-14 A | |
| L03-7020 | HVAC Rough-In | 1 | 0 | 29-Jun-14 A | 15-Jul-14 A | |
| L1RR-8100 | Insulation [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8100 | Insulation [DELETED - included in Ballroom activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8100 | Insulation [DELETED - included in Meeting Rooms ac | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8102 | GWB Hang [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8215 | GWB Tape [DELETED - included in Meeting Rooms a | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8104 | Prime Paint [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8102 | GWB Hang [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8215 | GWB Tape [DELETED - included in Ballroom activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8104 | Prime Paint [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |

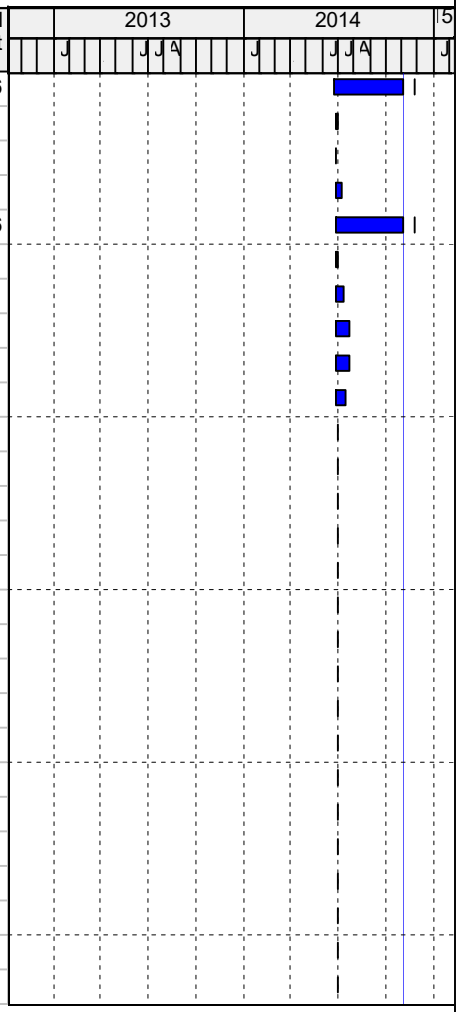



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1RR-8102 | GWB Hang [DELETED - included in Kitchen activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8215 | GWB Tape [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8104 | Prime Paint [DELETED - included in Kitchen activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L03-7018 | Electrical Rough-In | 1 | 0 | 01-Jul-14 A | 14-Jul-14 A | |
| L03-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Jul-14 A | 15-Jul-14 A | |
| L10-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7102 | Install Vertical Heat Pump | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L03-7116 | Frame Walls | 1 | 0 | 02-Jul-14 A | 14-Jul-14 A | |
| L03-7118 | Install HM Door Frame | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L04-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L05-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L07-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L08-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L09-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L10-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L12-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| I-3708 | Complete wall framing at Stair/Elevator 5 (LL3) | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |

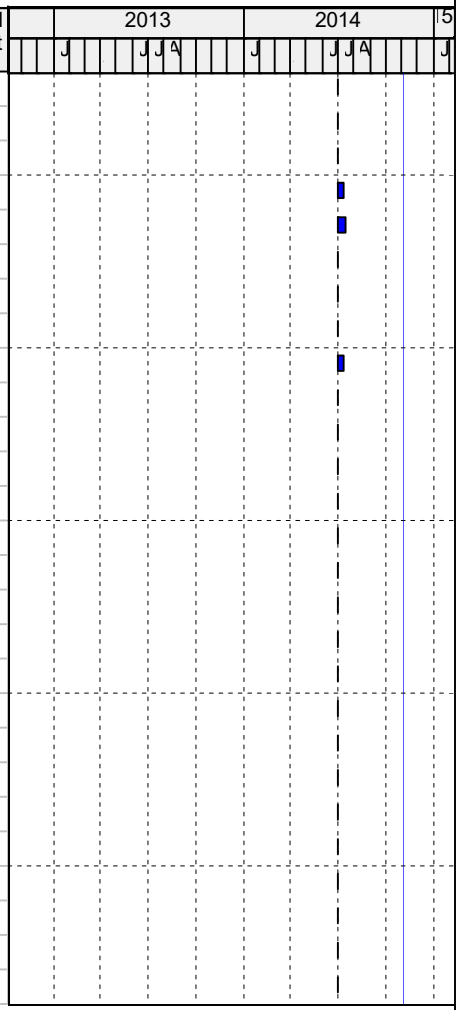



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L11-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 03-Jul-14 A | 07-Jul-14 A | |
| L04-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L05-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L06-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L07-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L08-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L17-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L10-6040 | Test Heat Pumps - L7, L8, L9 and L10 | 3 | 0 | 07-Jul-14 A | 09-Jul-14 A | |
| L10-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L03-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L04-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L05-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L06-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L07-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L08-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L09-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L10-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L12-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |

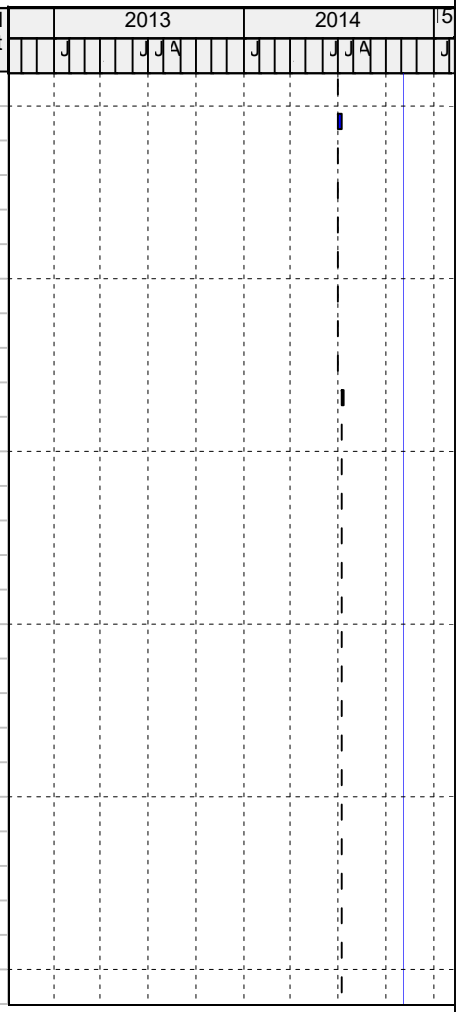



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L11-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Jul-14 A | 29-Jul-14 A | |
| L03-8602 | L3 Pool - Fire Sprinkler R/I | 5 | 0 | 08-Jul-14 A | 22-Jul-14 A | |
| L03-7016 | Install HM door frame | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L11-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L16-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 09-Jul-14 A | |
| L04-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |

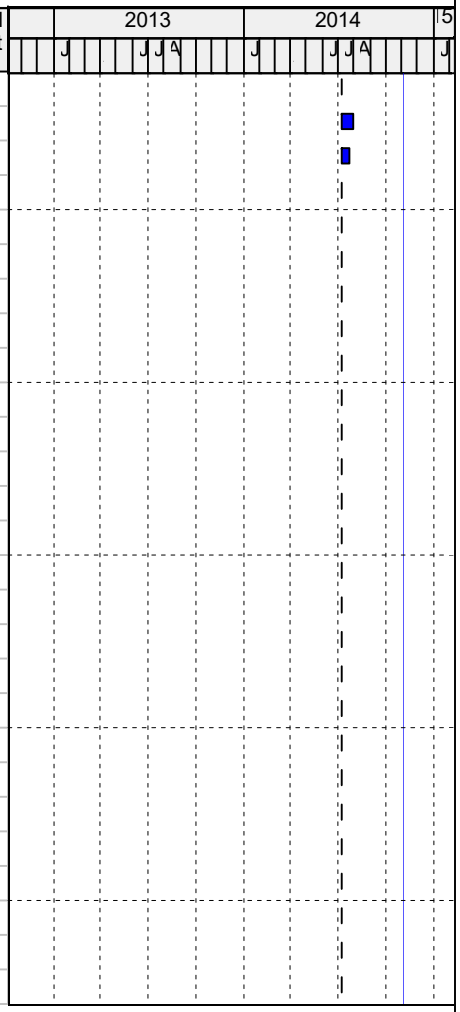



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L12-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| MP-FAB1 | Fabricate and Deliver Bronze Gold Horizontal Panels | 30 | 0 | 09-Jul-14 A | 15-Jul-14 A | |
| L04-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L05-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L06-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L16-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| MP-FAB2 | Fabricate and Deliver Silver Vertical Panels | 45 | 0 | 10-Jul-14 A | 25-Aug-14 A | |
| I-3004 | Issue ASI 38 | 0 | 0 | 11-Jul-14 A | | |
| I-3006 | Release bar area for x-ray examination | 5 | 0 | 11-Jul-14 A | 03-Sep-14 A | |
| L07-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| LL1-Z2-6018a | Complete Mech RI at tower crane opening (LL1) | 4 | 0 | 14-Jul-14 A | 17-Jul-14 A | |
| L08-6223 | Frame Corridor Ceilings | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| SW-2006a | Complete Dry Utilities (Phase 2) | 5 | 0 | 14-Jul-14 A | 24-Jul-14 A | |
| L04-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L04-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L05-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L06-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |

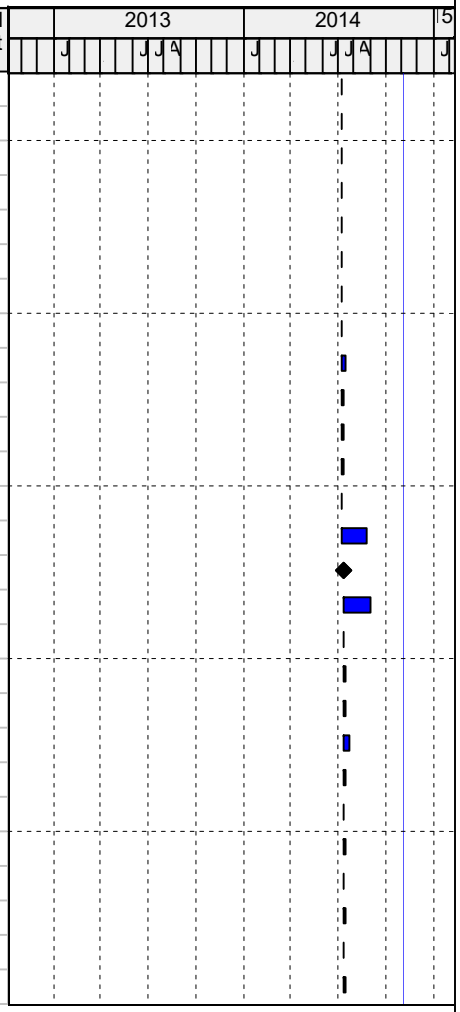



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L04-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L11-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L11-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L12-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L12-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L15-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L15-7102 | Install Vertical Heat Pump | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L1B-6026 | Install operable partition steel | 2 | 0 | 15-Jul-14 A | 08-Aug-14 A | |
| L09-6223 | Frame corridor ceilings | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L03-7120 | Electrical Rough-In | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |

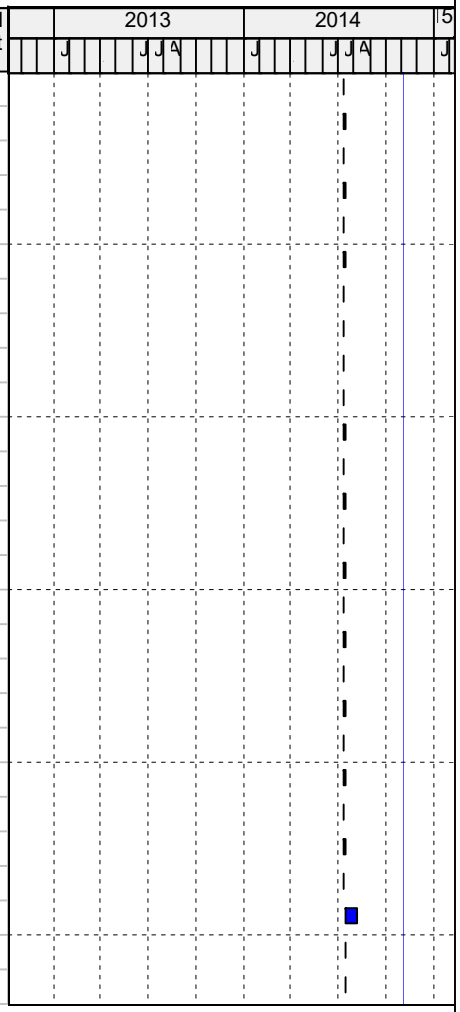



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L07-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L08-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L08-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L09-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L09-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L03-7142 | Install Laundry Chute (All Levels) | 9 | 0 | 15-Jul-14 A | 25-Jul-14 A | |
| LL2-2045 | LL2 - Electrical Room build-out | 15 | 0 | 15-Jul-14 A | 26-Sep-14 A | |
| L03-7122 | HVAC Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L04-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L05-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L06-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L07-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L07-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L08-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L08-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L09-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L09-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |

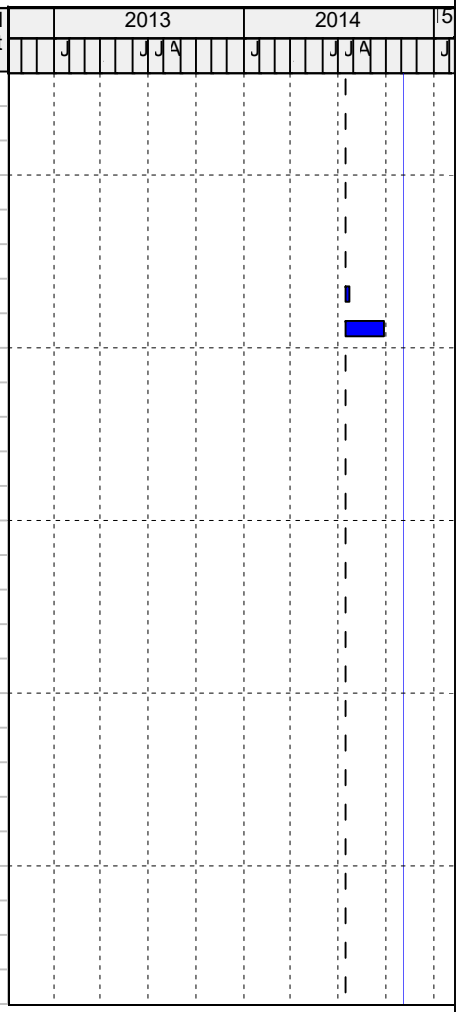



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L11-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L11-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L12-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L12-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L15-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L15-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L16-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L17-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L04-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L04-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L05-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L05-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L06-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L06-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L07-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L08-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L09-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |

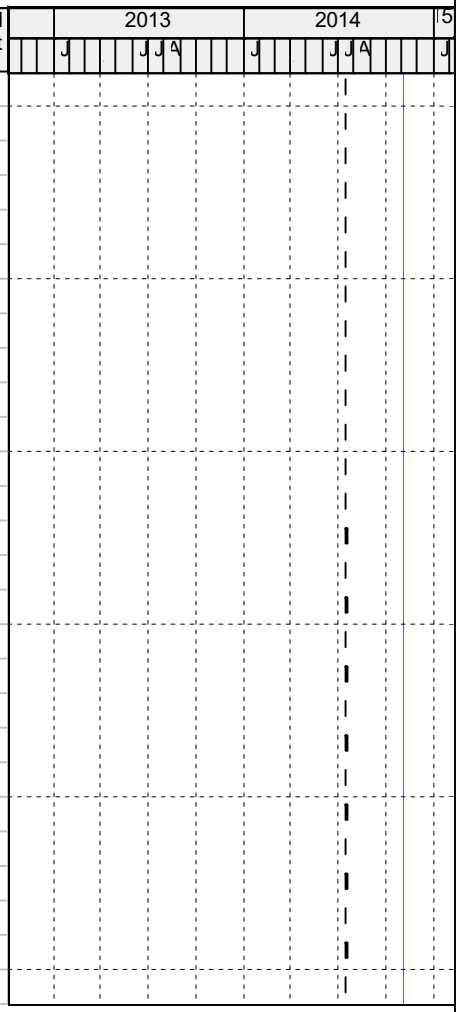



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L11-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L11-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L12-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L12-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L16-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L03-8608 | L3 Pool - Electrical R/I | 5 | 1 | 18-Jul-14 A | 25-Nov-14 | 16 |
| L03-8610 | L3 Pool - Fire Alarm / Elec Specialties R/I | 5 | 1 | 18-Jul-14 A | 25-Nov-14 | 16 |
| L15-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L15-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| L17-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L17-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| LL2-2052 | LL2 - Install fuel piping and exhaust duct to Generatc | 8 | 0 | 21-Jul-14 A | 15-Aug-14 A | |
| L04-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L04-7016 | Install HM door frame | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L07-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L08-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L10-7116 | Frame Walls | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L16-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 21-Jul-14 A | 22-Jul-14 A | |
| L16-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |

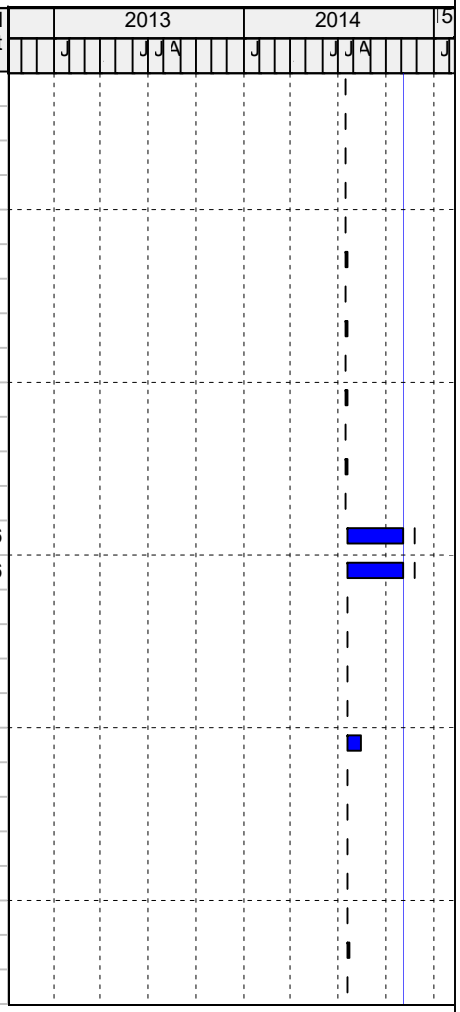



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| MPT-1002 | Tower - Install Elevation 35 (east elevation-south half) | 8 | 0 | 25-Jul-14 A | 04-Aug-14 A | |
| L16-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 25-Jul-14 A | 25-Jul-14 A | |
| L11-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L14-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L15-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L16-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L10-6223 | Frame Corridor Ceilings | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L11-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L15-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L15-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L11-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L14-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L16-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| I-1304 | Prep Kitchen - Additional framing (ASI 30) | 2 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-2302 | Framing "Go Back" work at LL1 for RFI 233 | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| I-2502 | Electrical rework at LL1 for ASIs 7, 9r2, 14, 27 | 4 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| L12-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L1B-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 01-Aug-14 A | 15-Aug-14 A | |
| MPL4-1000 | Upper L4 Ballroom - Install Elevations 1, 2 & 3 (south | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1000 | Tower - Install Elevations 26-27 (west elevation) [DEL | 13 | 0 | 01-Aug-14 A | 01-Aug-14 A | |

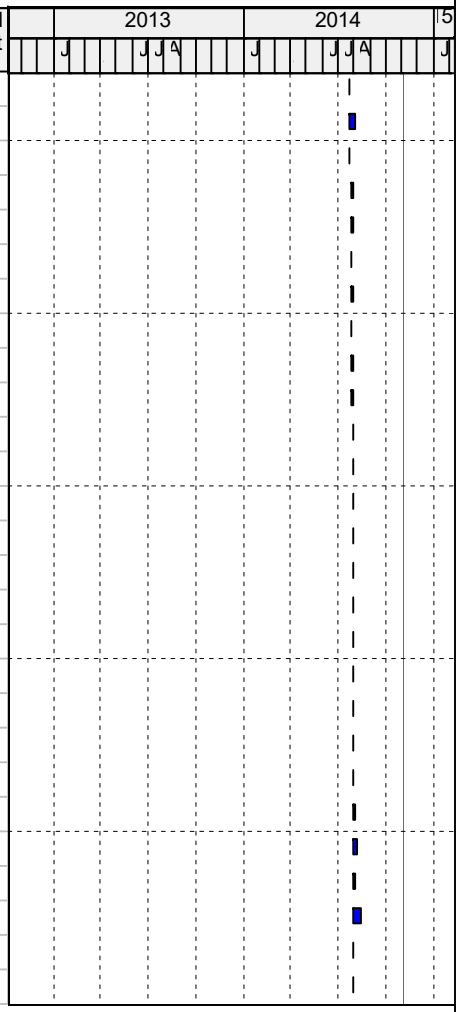



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPP-1002 | Podium - Install Elevations 1 & 2 (west elevation, sou | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPP-1008 | Podium - Install Elevations 7 & 8 (north & east elevati | 9 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1002 | Upper L4 Ballroom - Install Elevation 10 (west elevatic | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1004 | Upper L4 Ballroom - Install Elevation 9 (north elevatio | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1006 | Tower - Install Elevation 40 (east return-east end) [DE | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1010 | Tower - Install Elevations 51 (north elevation) [DELET | 8 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-4004 | East Stitched - Install metal panels [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L11-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L11-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L15-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L14-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L17-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| MPT-1010b | Tower - Install Elevation 45 [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L16-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 04-Aug-14 A | 05-Aug-14 A | |
| L11-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Aug-14 A | 08-Aug-14 A | |
| L04-7020 | HVAC Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |

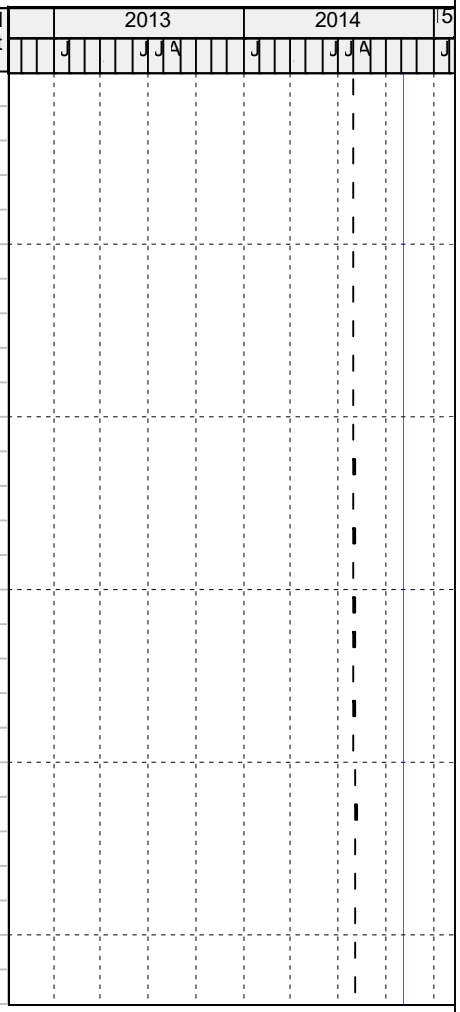



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L14-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L15-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 05-Aug-14 A | 07-Aug-14 A | |
| L05-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L06-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L07-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L08-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L09-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L10-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7018 | Electrical Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L14-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 05-Aug-14 A | 06-Aug-14 A | |
| L14-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| I-4104 | Install added trap primers - LL1 | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L06-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L07-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L08-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L09-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |

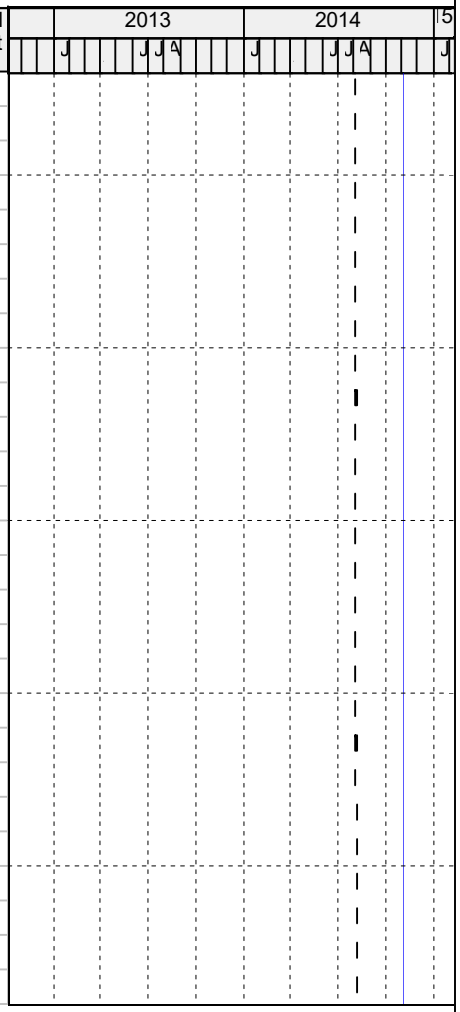



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7020 | HVAC Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L16-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| EL-1220 | Elevator fronts delivered | 0 | 0 | 07-Aug-14 A | | |
| L12-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L12-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-6223 | Frame Corridor Ceilings | 4 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L11-7016 | Install HM door frame | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L12-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L15-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L15-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L16-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L16-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L17-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L17-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-6040 | Test Heat Pumps - L11, L12 and L14 | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| PH-6026 | PH - Insulation/Vapor Barrier/GWB at Exterior Walls | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |

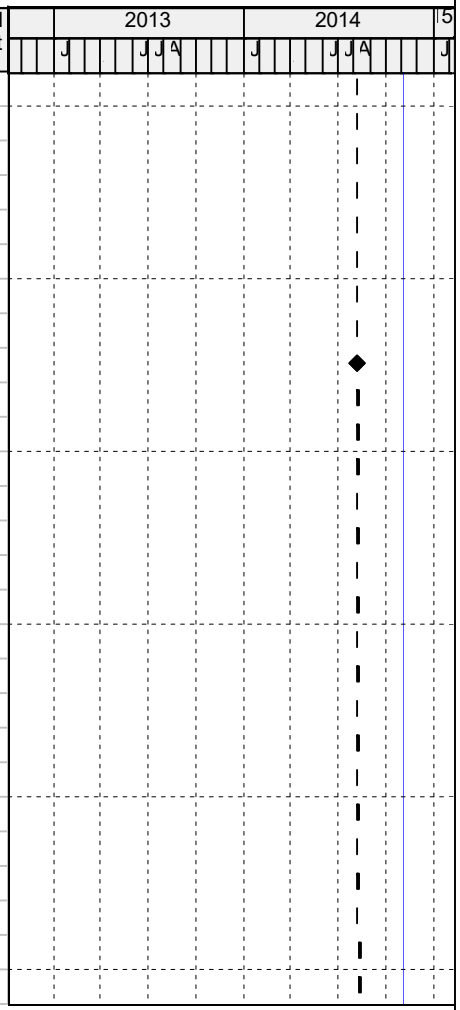



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L11-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-7026 | Inspections for GWB Cover | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 13-Aug-14 A | 13-Aug-14 A | |
| L15-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 14-Aug-14 A | 15-Aug-14 A | |
| LL2E-8108 | LL2 - Set fire pumps and equipment | 5 | 0 | 14-Aug-14 A | 29-Sep-14 A | |
| L10-7028 | GWB Hang/Tape/Finish | 5 | 2 | 14-Aug-14 A | 04-Nov-14 | 32 |
| L12-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L12-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L16-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L1BOH2-6008 | Int Wall Framing & Inspection | 5 | 0 | 14-Aug-14 A | 20-Aug-14 A | |
| I-4106 | Install added trap primers - L1 | 1 | 0 | 15-Aug-14 A | 15-Aug-14 A | |
| L14-6223 | Frame Corridor Ceilings | 4 | 0 | 15-Aug-14 A | 16-Aug-14 A | |
| L03-8136 | Install Counter Subtops | 3 | 0 | 15-Aug-14 A | 18-Aug-14 A | |
| LL2-2054 | LL2 - GWB, Hang 1st Layer at Laundry Room | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| LL2E-8112 | LL2 - Form/Pour Fire Pump Pads/Curbs | 2 | 0 | 16-Aug-14 A | 18-Aug-14 A | |
| LL1-6014Ia | L1 bar redesign - rework plumbing at ceilings | 10 | 5 | 18-Aug-14 A | 07-Nov-14 | 3 |

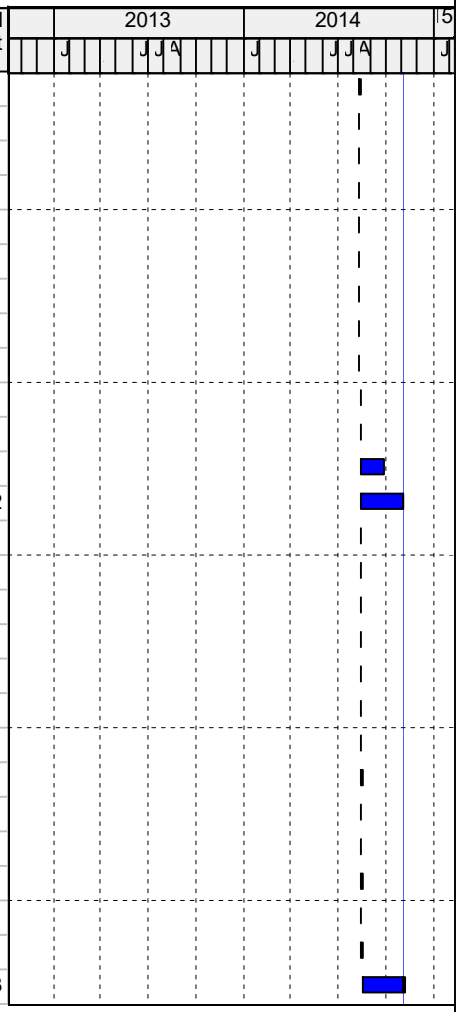



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6223 | Frame Corridor Ceilings | 4 | 0 | 18-Aug-14 A | 21-Aug-14 A | |
| L17-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Aug-14 A | 18-Aug-14 A | |
| L04-8136 | Install Counter Subtops | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-6014Ic | L1 bar redesign - rework electrical at ceilings | 10 | 5 | 18-Aug-14 A | 07-Nov-14 | 4 |
| LL2E-8114 | LL2 - Set Tube Steel at Door | 1 | 0 | 19-Aug-14 A | 19-Aug-14 A | |
| L17-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 20-Aug-14 A | 21-Aug-14 A | |
| L17-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 20-Aug-14 A | 20-Aug-14 A | |
| L05-8136 | Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 26-Aug-14 A | |
| L06-8136 | Bathrooms - Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 13-Oct-14 A | |
| L16-6223 | Frame Corridor Ceilings | 4 | 0 | 21-Aug-14 A | 29-Aug-14 A | |
| L17-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 21-Aug-14 A | 22-Aug-14 A | |
| L17-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 21-Aug-14 A | 21-Aug-14 A | |
| L1BOH2-6016 | Electrical RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6018 | HVAC RI | 4 | 0 | 21-Aug-14 A | 17-Oct-14 A | |
| L15-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7020 | HVAC Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7022 | Fire Sprinkler Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| LL2E-8116 | LL2 - Set Door Jamb | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L04-7028 | GWB Hang/Tape/Finish | 5 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L05-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L05-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L06-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |

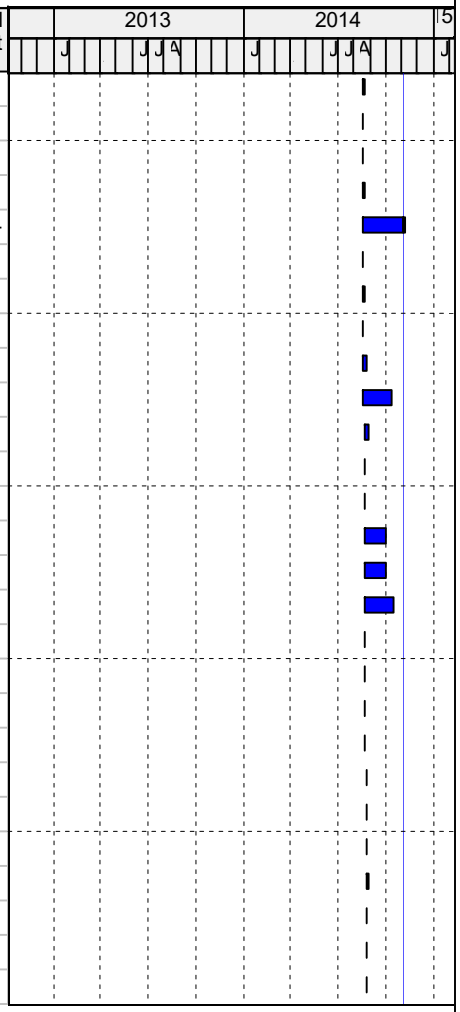



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L03-8123 | Bathroom "Barn Doors" On Site | 0 | 0 | 25-Aug-14 A | | |
| LL3-6026 | LL3 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL2-6026 | LL2 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL1-Z3-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L1BOH2-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |

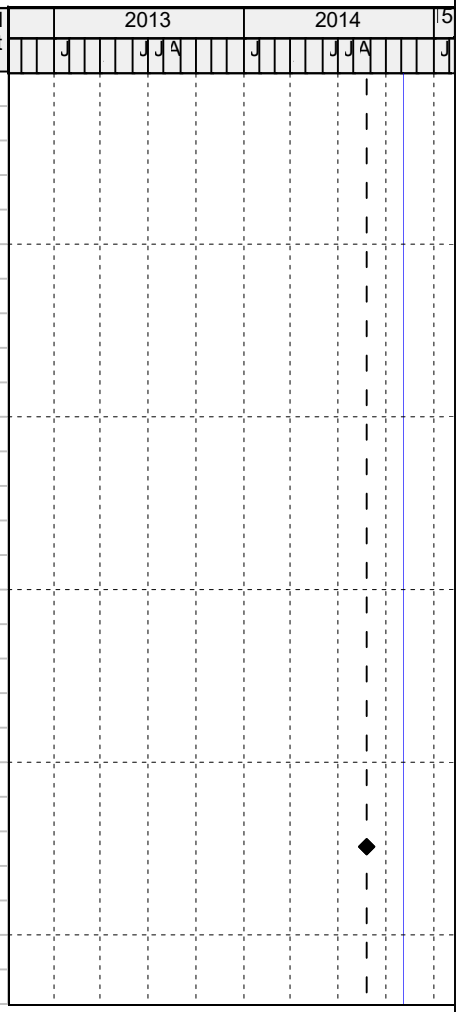



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-6026 | L2 - Set Elevator Fronts (Cars 1-4 | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L03-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L04-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L05-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L06-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L07-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L08-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L09-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L10-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L11-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L12-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L14-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L15-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L16-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L17-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| MPT-1008 | Tower - Install E/W Wing, N. Side West Half (Elev 50,: | 7 | 0 | 26-Aug-14 A | 03-Oct-14 A | |
| L06-6005 | CMU Fire Caulk/Clips | 2 | 1 | 26-Aug-14 A | 03-Nov-14 | 44 |
| L07-6005 | CMU Fire Caulk/Clips | 2 | 1 | 26-Aug-14 A | 03-Nov-14 | 44 |
| L08-6005 | CMU Fire Caulk/Clips | 2 | 1 | 26-Aug-14 A | 03-Nov-14 | 44 |
| L05-7026 | Inspections for GWB Cover | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L05-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L11-7028 | GWB Hang/Tape/Finish | 5 | 2 | 26-Aug-14 A | 04-Nov-14 | 33 |
| L12-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L14-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L03-8105a | Painting - Split Door Jambs | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L09-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 03-Nov-14 | 44 |
| L10-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 03-Nov-14 | 44 |

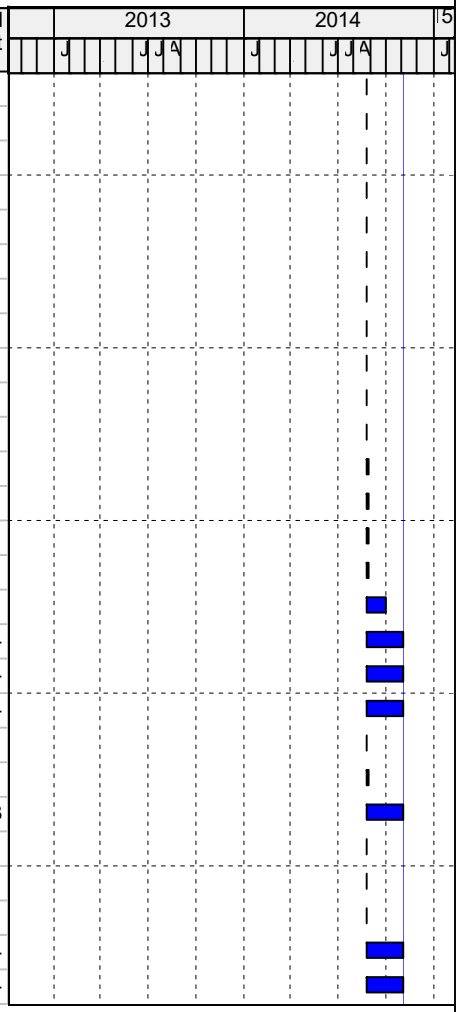


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 04-Nov-14 | 44 |
| L12-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 04-Nov-14 | 44 |
| L14-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 04-Nov-14 | 44 |
| L15-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 04-Nov-14 | 44 |
| L16-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 04-Nov-14 | 44 |
| L05-8201 | Install ACT Grid @ Corridors | 2 | 0 | 27-Aug-14 A | 28-Aug-14 A | |
| L16-7022 | Fire Sprinkler Rough-In | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L04-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L06-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| EP-5110a | L1 - Install Steel at Revolving Door Opening | 3 | 0 | 27-Aug-14 A | 29-Aug-14 A | |
| L05-8105a | Painting - Split Door Jambs | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| I-4102 | Install added trap primers - LL2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4108 | Install added trap primers - L2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4110 | Install added trap primers - L3 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4112 | Install added trap primers - Roof PH | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| L03-8124d | Flooring On Site and Acclimated | 2 | 0 | 29-Aug-14 A | 01-Sep-14 A | |
| L02-5102 | L2 - Storefront Frames | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| L04-6005 | CMU Fire Caulk/Clips | 2 | 1 | 02-Sep-14 A | 03-Nov-14 | 44 |
| L05-6005 | CMU Fire Caulk/Clips | 2 | 1 | 02-Sep-14 A | 03-Nov-14 | 44 |
| L17-6005 | CMU Fire Caulk/Clips | 2 | 1 | 02-Sep-14 A | 04-Nov-14 | 44 |
| L03-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L12-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L14-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L07-8136 | Install Counter Subtops | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| LL1-Z3-FCC10 | FCC - Set Jamb | 1 | 0 | 02-Sep-14 A | 03-Sep-14 A | |
| MPT-1004 | Tower - Install E/W Wing, S. Side w/o Windows (Elev | 10 | 0 | 03-Sep-14 A | 17-Oct-14 A | |
| L03-7028 | GWB Hang/Tape/Finish | 5 | 2 | 03-Sep-14 A | 04-Nov-14 | 25 |

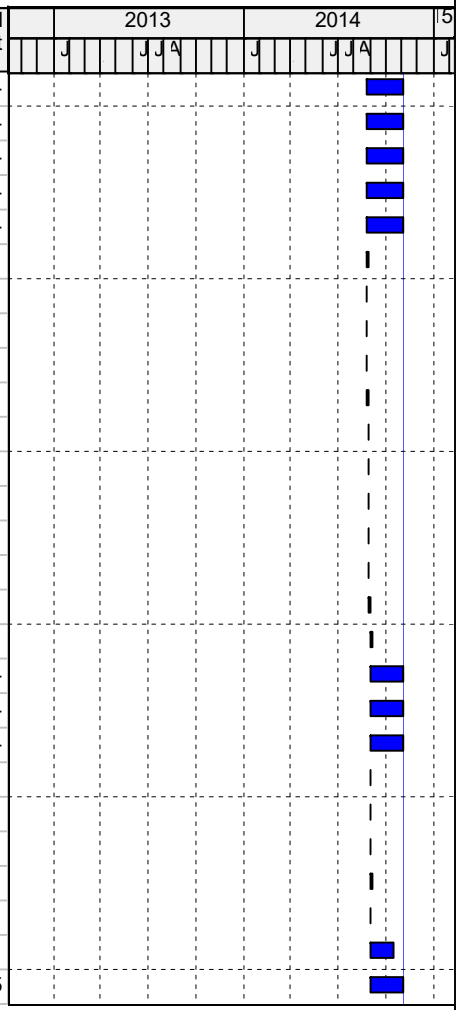



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7028 | GWB Hang/Tape/Finish | 5 | 2 | 03-Sep-14 A | 04-Nov-14 | 34 |
| L03-8126a | Doors & Hardware On Site | 0 | 0 | 03-Sep-14 A | | |
| LL1-Z3-FCC12 | FCC - Sheetrock Outside Wall | 1 | 0 | 03-Sep-14 A | 03-Sep-14 A | |
| L16-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| L17-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Sep-14 A | 11-Sep-14 A | |
| L02-5104b | L2 - Install Storefront Temporary Enclosures | 1 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| LL1-Z3-FCC14 | FCC - Verify Fire Caulk OK & Inspect Room OK to 2n | 1 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| I-3008 | Coordinate and perform x-ray examination | 7 | 0 | 04-Sep-14 A | 12-Sep-14 A | |
| L02-5104a | L2 - Measure/Fabricate Storefront Glazing | 15 | 0 | 05-Sep-14 A | 18-Sep-14 A | |
| LL1-Z3-FCC16 | FCC - GWB, Hang 2nd Layer | 2 | 0 | 05-Sep-14 A | 08-Sep-14 A | |
| L03-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L15-7018 | Electrical Rough-In | 1 | 0 | 08-Sep-14 A | 08-Sep-14 A | |
| EL-1228 | Construct/Approve elevator lobby framing mockup (L | 3 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| LL2E-8118 | LL2 - Frame Infill, Install Densglass & Inspect at Fire I | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L06-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L08-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L15-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7018 | Electrical Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L3-5104a | L3 - Measure/Fabricate Storefront Glazing | 15 | 0 | 09-Sep-14 A | 30-Sep-14 A | |
| L03-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 23-Sep-14 A | |
| L03-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L04-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L06-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| L08-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |

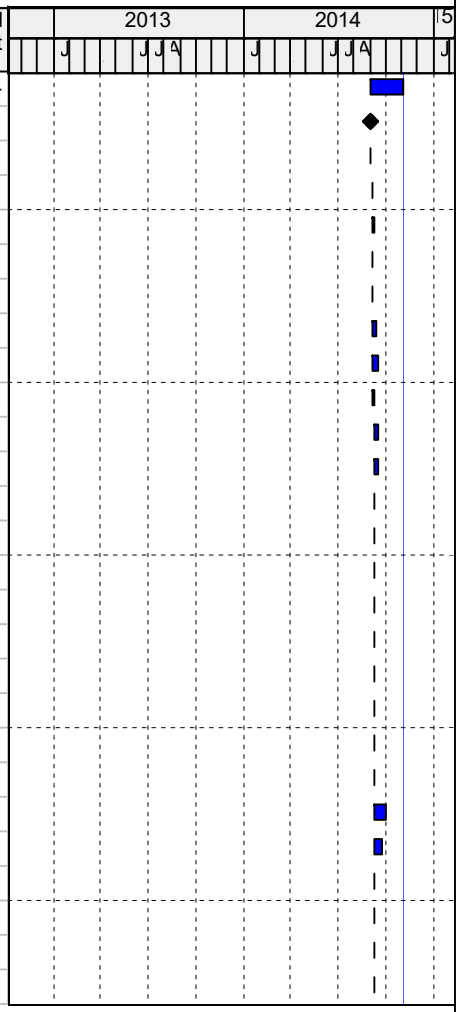



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L06-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L06-7028 | GWB Hang/Tape/Finish | 5 | 2 | 10-Sep-14 A | 04-Nov-14 | 28 |
| L08-7028 | GWB Hang/Tape/Finish | 5 | 2 | 10-Sep-14 A | 04-Nov-14 | 30 |
| L15-7026 | Inspections for GWB Cover | 1 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| LL2E-8120 | LL2 - Insulation, Vapor Barrier & Inspect at Fire Pump | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L08-8395 | Framing at Elevator Lobby | 4 | 0 | 11-Sep-14 A | 17-Sep-14 A | |
| L15-7028 | GWB Hang/Tape/Finish | 5 | 2 | 11-Sep-14 A | 04-Nov-14 | 36 |
| L08-8136 | Install Counter Subtops | 3 | 0 | 11-Sep-14 A | 16-Sep-14 A | |
| L02-6025 | L2 - Framing Go-Back Work (left out for mechanical e | 4 | 0 | 11-Sep-14 A | 02-Oct-14 A | |
| L1-5104a | L1 - Measure/Fabricate Storefront Glazing | 15 | 0 | 12-Sep-14 A | 18-Sep-14 A | |
| L1B-8102c | Finish framing and MEP at Main Ballroom East Wall ( | 10 | 0 | 12-Sep-14 A | 02-Oct-14 A | |
| L09-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L10-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L11-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L12-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L16-7026 | Inspections for GWB Cover | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| MPT-1014 | Tower - Install E/W Wing, N. Side, E. Half (Elev 46-49 | 8 | 0 | 15-Sep-14 A | 28-Oct-14 A | |
| LL2-6032 | LL2 - Complete Framing (Including Elevator Lobby) | 4 | 0 | 15-Sep-14 A | 18-Sep-14 A | |
| L1-5104b | L1 - Install Storefront Temporary Enclosures | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| LL1-Z3-FCC18 | FCC - Install Temp Door | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| LL2-2058a | LL2 - GWB Hang 1st Layer | 5 | 0 | 15-Sep-14 A | 19-Sep-14 A | |
| LL2-2064 | LL2 - Generator Room - Finish Exhaust Piping | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| I-3010 | Prepare proposal for MEP relocations | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| L16-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L07-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |

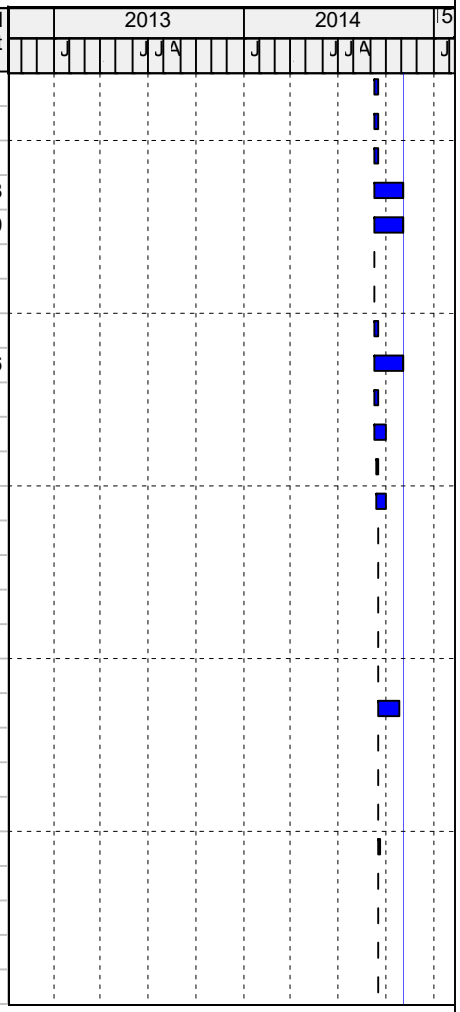



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L10-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L14-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L15-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L03-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| L16-7028 | GWB Hang/Tape/Finish | 5 | 2 | 16-Sep-14 A | 04-Nov-14 | 37 |
| L17-7018 | Electrical Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L09-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L10-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| LL3-6028 | LL3 - Frame Elevator Lobby | 2 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| LL4-6026 | LL4 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| I-3012 | Owner approve proposal for MEP relocations | 3 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| L11-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L12-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L14-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L15-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L04-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L17-7026 | Inspections for GWB Cover | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L17-7116 | Frame Walls | 4 | 0 | 17-Sep-14 A | 29-Sep-14 A | |
| LL2-2066 | LL2 - Generator Room - Finish Fuel Piping | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L16-8395 | Framing at Elevator Lobby | 4 | 0 | 18-Sep-14 A | 26-Sep-14 A | |
| L02-5104 | L2 - Storefront Glazing | 2 | 0 | 18-Sep-14 A | 22-Sep-14 A | |
| L17-7028 | GWB Hang/Tape/Finish | 5 | 2 | 18-Sep-14 A | 04-Nov-14 | 38 |
| LL4-6028 | LL4 - Frame Elevator Lobby | 2 | 0 | 18-Sep-14 A | 02-Oct-14 A | |
| MPT-1010a | Tower - Install E/W Wing, West End (Elev 52,53) | 8 | 0 | 18-Sep-14 A | 10-Oct-14 A | |
| LL2-2068 | LL2 - Generator Room - Electrical Finishes | 3 | 0 | 19-Sep-14 A | 30-Sep-14 A | |

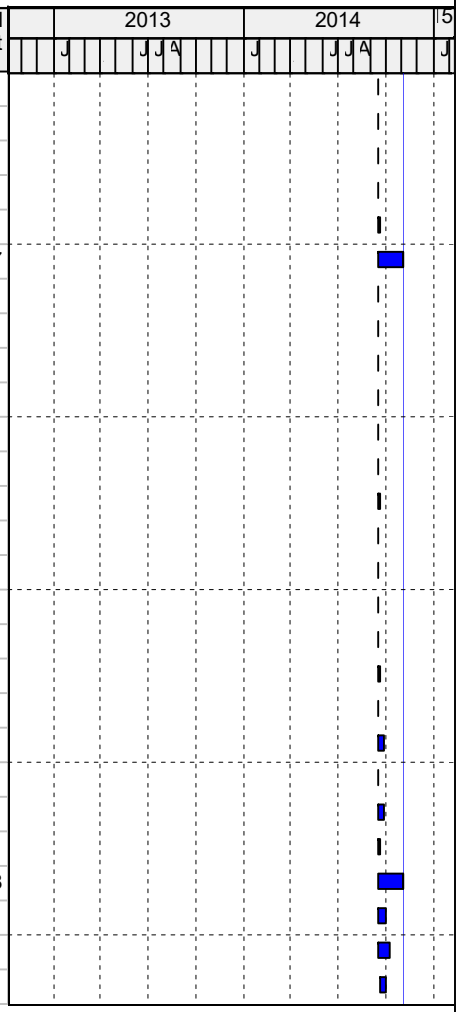



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L09-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L04-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L05-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L03-8140 | Countertops On Site | 0 | 0 | 22-Sep-14 A | | |
| L03-8129a | Shower Doors On Site | 0 | 0 | 22-Sep-14 A | | |
| LL1-Z3-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L1BOH2-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2-2048a | LL2 - Move in Laundry Room Ironer | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2E-8122 | LL2 - Hang GWB at Fire Pump Room | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-FCC20 | FCC - Rough-In and Install Panels | 25 | 2 | 22-Sep-14 A | 04-Nov-14 | 48 |
| I-3014 | Core drill for MEP relocations | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L05-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L07-7028 | GWB Hang/Tape/Finish | 5 | 2 | 23-Sep-14 A | 04-Nov-14 | 29 |
| L09-7028 | GWB Hang/Tape/Finish | 5 | 2 | 23-Sep-14 A | 04-Nov-14 | 31 |
| L14-7028 | GWB Hang/Tape/Finish | 5 | 2 | 23-Sep-14 A | 04-Nov-14 | 35 |
| L04-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L05-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L06-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L07-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L04-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L06-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L04-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |

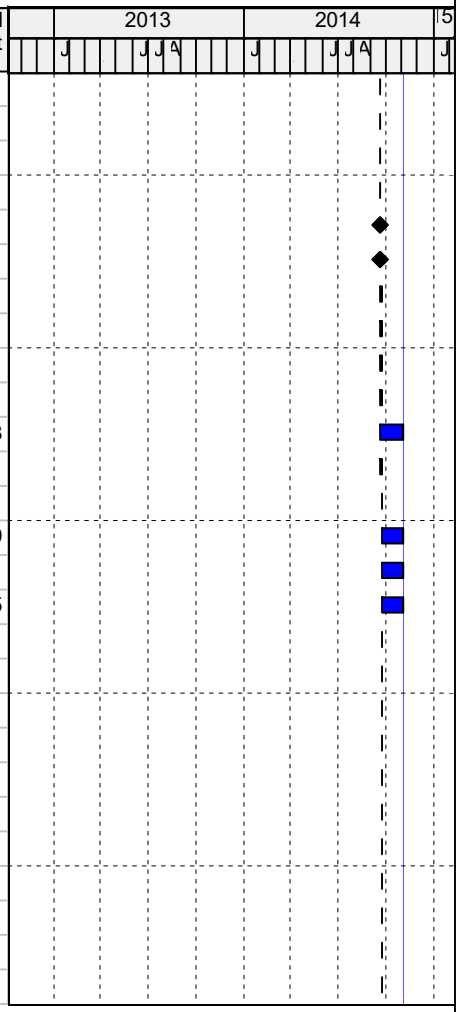



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-7122 | HVAC Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| LL2-2058 | LL2 - Tape/Finish Laundry Room | 3 | 0 | 24-Sep-14 A | 26-Sep-14 A | |
| L08-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L17-8395 | Framing at Elevator Lobby | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L05-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L06-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L07-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L08-7120 | Electrical Rough-In | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| LL2E-8124 | LL2 - Temp-In Louver Opening at Fire Pump Room | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L1-5104c | L1 - Install Storefront at Main Entry Facade | 5 | 0 | 25-Sep-14 A | 10-Oct-14 A | |
| L16-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L08-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L10-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L16-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L17-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L17-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L09-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L11-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |

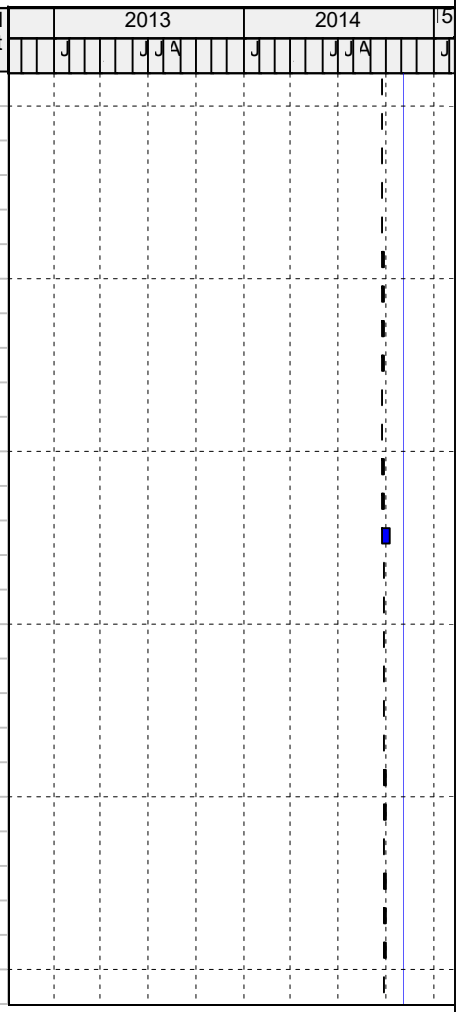



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L14-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L15-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L17-7118 | Install HM Door Frame | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| LL3-6030 | LL3 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL4-6030 | LL4 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL2-6034 | LL2 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L1BOH2-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L02-6030 | L2 - Framing at Elevator Lobby & North Half | 4 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| MPT-1022 | Tower - Caulking, west | 8 | 1 | 29-Sep-14 A | 03-Nov-14 | 28 |
| PH-6015 | PH - Set Boilers and Pumps | 12 | 0 | 29-Sep-14 A | 15-Oct-14 A | |
| L11-8204 | Bathrooms - Vinyl Wall Coverings | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L10-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L17-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L11-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L12-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L07-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 30-Sep-14 A | 08-Oct-14 A | |
| L11-8201 | Install ACT Grid @ Corridors | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L09-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L09-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L11-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L12-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L14-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L15-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| LL2-2072 | Generator - Complete generator and annunciator cor | 5 | 0 | 30-Sep-14 A | 21-Oct-14 A | |

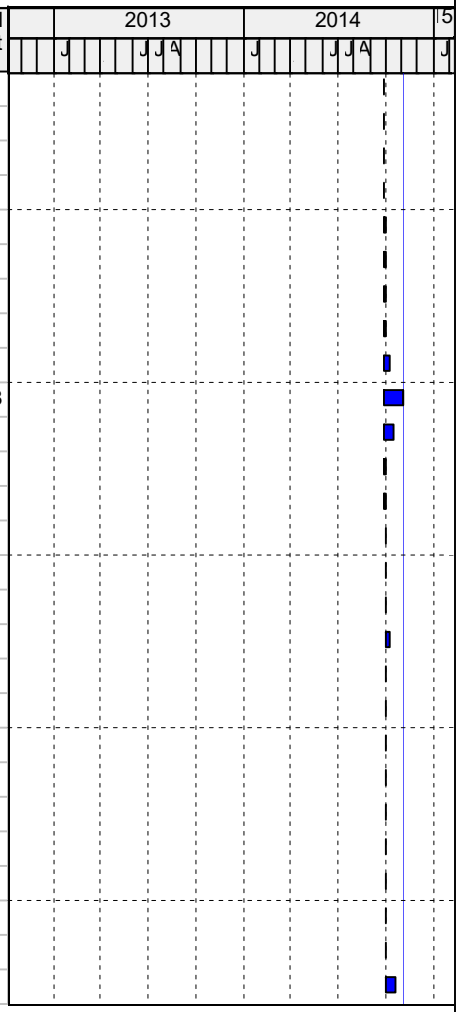



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6040 | Test Heat Pumps - L16 and L17 | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L17-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L14-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L03-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |

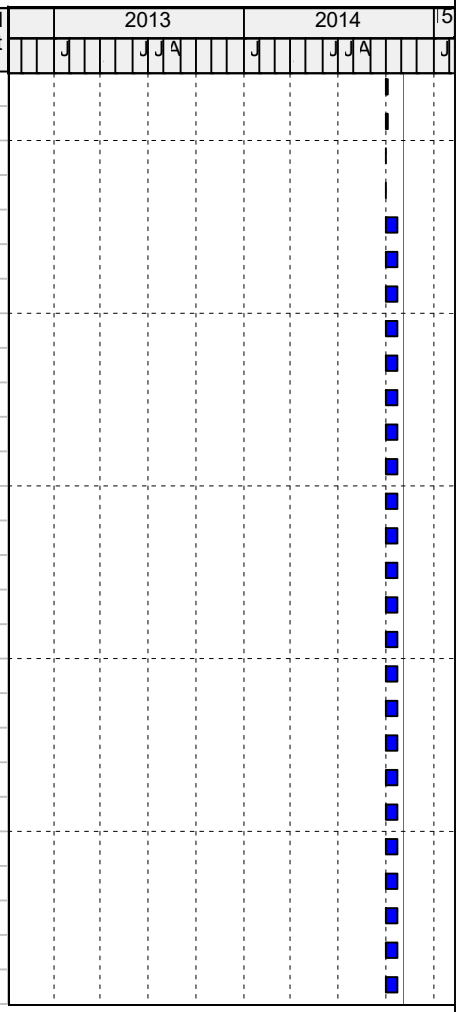



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L11-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L12-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L12-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L14-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L16-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L17-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L09-8136 | Install Counter Subtops | 3 | 0 | 01-Oct-14 A | 03-Oct-14 A | |
| L02-6032 | L2 - Electrical RI at Elevator Lobby & North Half | 5 | 0 | 01-Oct-14 A | 08-Oct-14 A | |
| LL1-Z3-FCC22 | FCC - Finishes | 10 | 3 | 01-Oct-14 A | 07-Nov-14 | 48 |
| SW-2306 | Prep, grind and overlay at 11th Ave, 3rd Place & 2nd | 5 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 01-Oct-14 A | 04-Nov-14 | 19 |

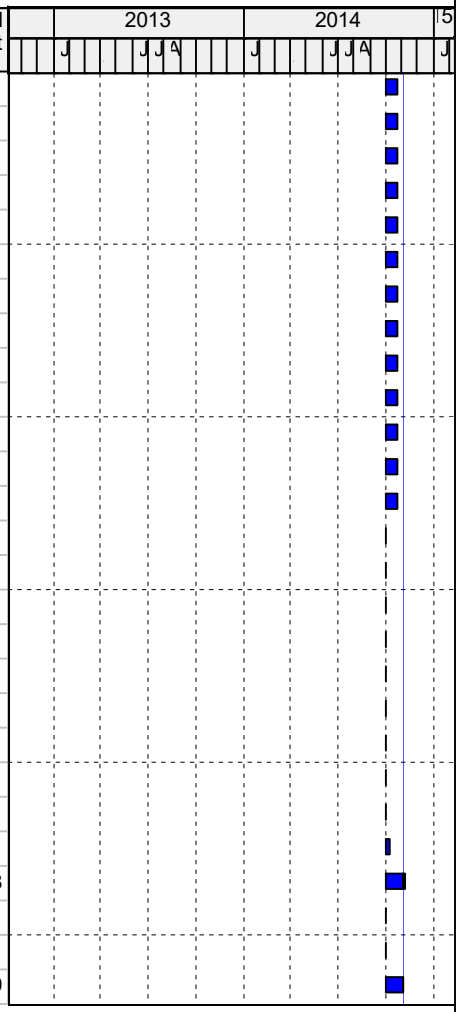



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L14-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L15-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1BOH2-8130 | Inspections For Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L02-6024a | L2 - Inspections - South Half | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L06-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| L17-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| LL2-2074 | Generator - Install fuel fill | 2 | 0 | 03-Oct-14 A | 06-Oct-14 A | |
| L07-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| MPT-1020 | Tower - Install E/W Wing, East End (Elev 41,44) | 5 | 0 | 06-Oct-14 A | 18-Oct-14 A | |
| LL1-8102a | GWB Hang/Tape (Ceilings) | 10 | 2 | 06-Oct-14 A | 04-Nov-14 | 11 |
| L1BOH2C-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6014 | Complete Plumbing RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6016 | Complete Electrical RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6018 | Complete HVAC RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L03-8200a | New murals on site (date estimated) | 0 | 0 | 06-Oct-14 A | | |
| SW-2100 | Zone 1 - Survey curb & site lighting | 2 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 06-Oct-14 A | 06-Oct-14 A | |
| L1BOH2-8100 | Insulation | 4 | 0 | 07-Oct-14 A | 13-Oct-14 A | |
| L17-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L12-8201 | Install ACT Grid @ Corridors | 2 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| L10-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 07-Oct-14 A | 20-Oct-14 A | |

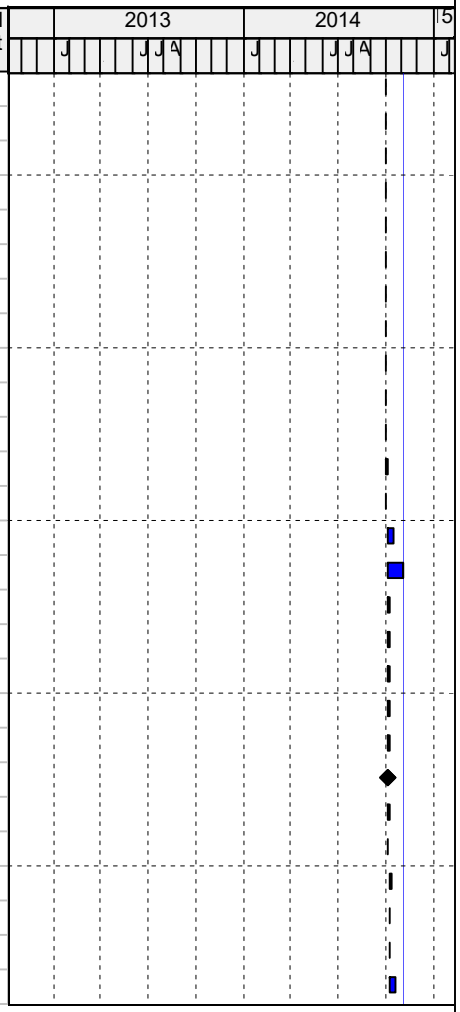



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-6032 | GWB Hang/Tape at Elevator Lobby | 5 | 2 | 07-Oct-14 A | 04-Nov-14 | 20 |
| L03-8216x | Vinyl Wall Coverings - Install Murals | 2 | 1 | 07-Oct-14 A | 03-Nov-14 | 26 |
| L1B-8102b | GWB Hang (Walls) & Inspection - Exterior Wall at Cor | 3 | 0 | 07-Oct-14 A | 09-Oct-14 A | |
| RF-4048 | Tower Roof - Install davit arms | 3 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| LL2-2076 | Generator - Install fuel fill mechanical piping | 4 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L12-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L09-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L03-8633 | Pool - Install waterproofing & test | 3 | 0 | 08-Oct-14 A | 17-Oct-14 A | |
| L03-8130 | Install Door Hardware | 3 | 0 | 08-Oct-14 A | 28-Oct-14 A | |
| L10-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L02-8102a | L2 - GWB Hang / Tape / Finish - South Half | 7 | 0 | 09-Oct-14 A | 27-Oct-14 A | |
| SW-2102 | Zone 1 - Vacate SE corner | 2 | 0 | 09-Oct-14 A | 11-Oct-14 A | |
| SW-2106 | Zone 1 - Sawcut and remove asphalt | 4 | 0 | 09-Oct-14 A | 14-Oct-14 A | |
| L11-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 09-Oct-14 A | |
| SW-2200 | Zone 2 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |
| SW-2300 | Zone 3 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |
| SW-2108 | Zone 1 - Install east footing drain | 4 | 0 | 10-Oct-14 A | 20-Oct-14 A | |
| L04-8130 | Install Door Hardware | 3 | 0 | 10-Oct-14 A | 29-Oct-14 A | |
| ML-5962 | Man/Material Lifts - Remove Roof Lift Stop | 0 | 0 | | 11-Oct-14 A | |
| I-1102 | Additional work at new L17 guest rooms | 5 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| LL2-2046 | LL2 - Generator Room - Misc. Finishes | 3 | 2 | 13-Oct-14 A | 04-Nov-14 | 50 |
| RF-4008 | Tower Roof - Install corrugated metal panels | 5 | 2 | 13-Oct-14 A | 04-Nov-14 | 31 |
| MPT-1018b | Tower - Roof cornice frame & sheath | 6 | 0 | 13-Oct-14 A | 24-Oct-14 A | |
| L02-8100a | L2 - Insulation - South Half | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| SW-2112 | Zone 1 - Grade for curb and gutter | 3 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| SW-2202 | Zone 2 - Install site lighting | 5 | 3 | 13-Oct-14 A | 10-Nov-14 | 28 |
| SW-2204 | Zone 2 - Repave utility trenches | 4 | 0 | 13-Oct-14 A | 22-Oct-14 A | |

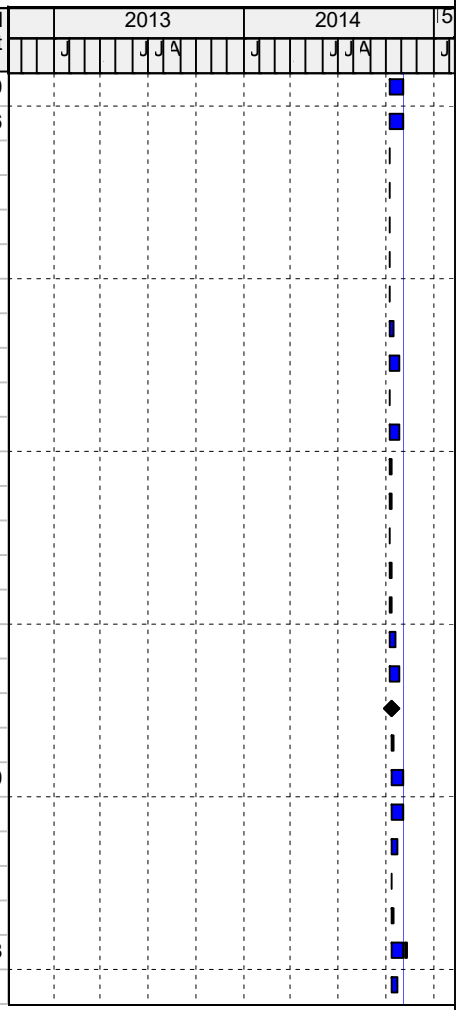



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 13-Oct-14 A | |
| SW-2302 | Zone 3 - Grade for curb and gutter | 2 | 1 | 14-Oct-14 A | 03-Nov-14 | 28 |
| L14-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 14-Oct-14 A | 16-Oct-14 A | |
| L05-8130 | Install Door Hardware | 3 | 1 | 14-Oct-14 A | 03-Nov-14 | 45 |
| L14-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 14-Oct-14 A | |
| L16-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L15-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 15-Oct-14 A | 17-Oct-14 A | |
| L15-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 15-Oct-14 A | |
| SW-2206 | Zone 2 - Grade for curb and gutter | 2 | 0 | 16-Oct-14 A | 20-Oct-14 A | |
| MPP-1000 | Podium - Install W/S/N Elevations (Elev 1-5, 6,9-19,2 | 10 | 8 | 20-Oct-14 A | 19-Nov-14 | 42 |
| L06-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 20-Oct-14 A | 23-Oct-14 A | |
| LL2-8106a | LL2 - Pinned Insulation @ Ramp Ceiling | 4 | 2 | 20-Oct-14 A | 04-Nov-14 | 34 |
| L1B-8102d | GWB Hang (Walls) & Inspection - Main Ballroom East | 1 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| SW-2114 | Zone 1 - FRP curb and gutter | 2 | 1 | 20-Oct-14 A | 10-Nov-14 | 26 |
| RF-4044 | Ballroom Roof - Install metal coping | 3 | 2 | 20-Oct-14 A | 10-Nov-14 | 31 |
| L08-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 21-Oct-14 A | 23-Oct-14 A | |
| MPT-1018 | Tower - Install Roof Penthouse (Elev 36b,37,38.39) | 5 | 3 | 21-Oct-14 A | 05-Nov-14 | 37 |
| L11-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2208 | Zone 2 - FRP curb and gutter | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2304 | Zone 3 - FRP curb and gutter | 3 | 2 | 21-Oct-14 A | 05-Nov-14 | 28 |
| SW-2308 | Zone 3 - Install site lighting | 5 | 3 | 21-Oct-14 A | 06-Nov-14 | 29 |
| L15-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |

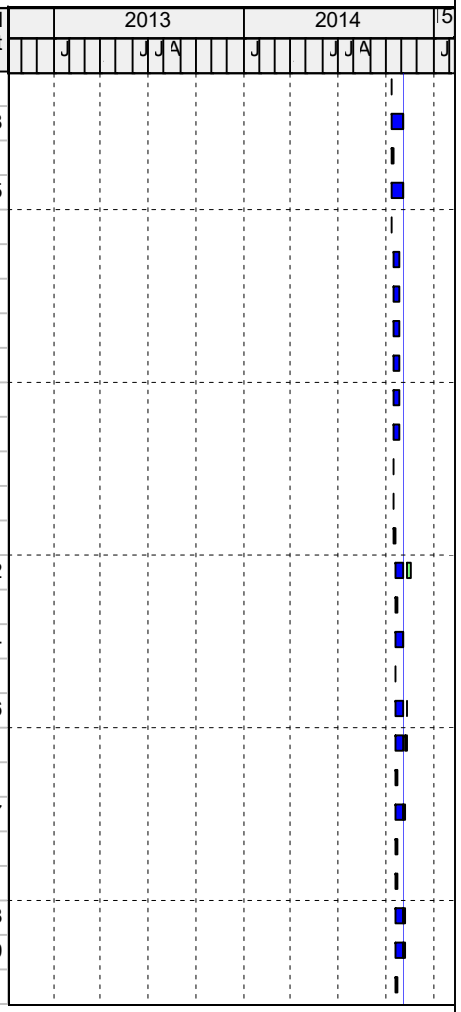



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8130 | Install Door Hardware | 3 | 1 | 21-Oct-14 A | 03-Nov-14 | 15 |
| L03-8634 | Pool - Install reinforcing steel & inspect | 5 | 0 | 22-Oct-14 A | 30-Oct-14 A | |
| MPT-1016 | Tower - Install N/S Wing, S. End W. of Manlift (Elev 2 | 5 | 3 | 22-Oct-14 A | 05-Nov-14 | 34 |
| SW-2116 | Zone 1 - Fine grade for sidewalk | 3 | 1 | 22-Oct-14 A | 11-Nov-14 | 27 |
| LL4-8106 | LL4 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| LL3-8106 | LL3 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L14-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L08-8130 | Install Door Hardware | 3 | 1 | 22-Oct-14 A | 05-Nov-14 | 15 |
| L07-8130 | Install Door Hardware | 3 | 1 | 22-Oct-14 A | 04-Nov-14 | 15 |
| L03-8606 | L3 Pool - HVAC R/I | 3 | 0 | 23-Oct-14 A | 27-Oct-14 A | |
| L09-8121 | Install Bathroom "Barn Doors" | 4 | 1 | 23-Oct-14 A | 03-Nov-14 | 17 |
| L12-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| LL2-2078 | Generator - Install fuel fill control wiring | 2 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| CO-7204 | Cx - Gas Service established | 0 | 0 | | 24-Oct-14 A | |
| L1BOH2-8102 | GWB Hang (Walls) | 4 | 3 | 27-Oct-14 A | 05-Nov-14 | 12 |
| L04-8216 | Vinyl Wall Coverings - Install Murals | 2 | 1 | 27-Oct-14 A | 04-Nov-14 | 26 |
| LL2-2080 | Generator - Complete generator accessories (battery) | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| LL2-2082 | Generator - Cx fuel fill | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| L09-8130 | Install Door Hardware | 3 | 1 | 28-Oct-14 A | 06-Nov-14 | 15 |
| CO-7158 | Generator - Interim electrical inspection | 1 | 0 | 29-Oct-14 A | 29-Oct-14 A | |
| LL2-2070 | LL2 - Generator Room - Generator Ready for Startup | 0 | 0 | | 30-Oct-14 A | |
| LL2-2084 | Generator - Initial fuel fill | 1 | 0 | 30-Oct-14 A | 30-Oct-14 A | |
| CO-7200 | Cx - Penthouse Mechanical Installation Complete | 0 | 0 | | 30-Oct-14 A | |
| L03-8636 | Pool - Shotcrete | 1 | 0 | 31-Oct-14 A | 31-Oct-14 A | |
| LL2E-8340 | LL2 - Install walk-in cooler/freezer (BY OTHERS) | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 13 |
| L03-8405 | Cover Inspection | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 8 |
| L04-8405 | Cover Inspection | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 16 |

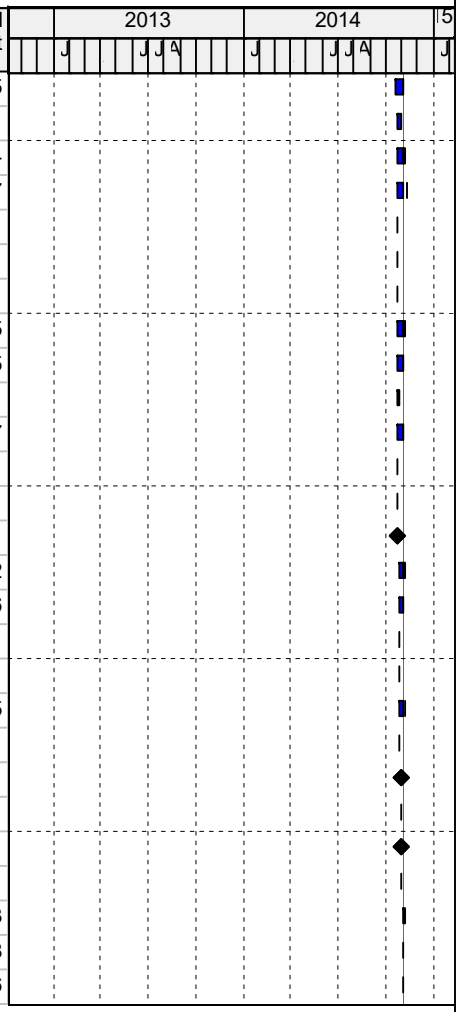



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8405 | Cover Inspection | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 11 |
| L06-8405 | Cover Inspection | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 20 |
| L07-8405 | Cover Inspection | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 14 |
| L08-8405 | Cover Inspection | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 24 |
| L09-8405 | Cover Inspection | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 17 |
| L10-8405 | Cover Inspection | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 26 |
| L11-8405 | Cover Inspection | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 20 |
| L12-8405 | Cover Inspection | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 26 |
| L14-8405 | Cover Inspection | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 23 |
| L15-8405 | Cover Inspection | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 26 |
| L16-8405 | Cover Inspection | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 26 |
| L17-8405 | Cover Inspection | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 26 |
| MPP-1010 | Podium - Install East Elevation (Elev 5 & 7) | 7 | 7 | 03-Nov-14 | 11-Nov-14 | 32 |
| L14-8201 | Corridors - Install ACT Grid | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 25 |
| L15-8201 | Corridors - Install ACT Grid | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 26 |
| L03-7128 | Inspections for GWB Cover | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 16 |
| L04-7128 | Inspections for GWB Cover | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 18 |
| L05-7128 | Inspections for GWB Cover | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 19 |
| L06-7128 | Inspections for GWB Cover | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 22 |
| L07-7128 | Inspections for GWB Cover | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 22 |
| L08-7128 | Inspections for GWB Cover | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 26 |
| L09-7128 | Inspections for GWB Cover | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 25 |
| L10-7128 | Inspections for GWB Cover | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 30 |
| L11-7128 | Inspections for GWB Cover | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 28 |
| L12-7128 | Inspections for GWB Cover | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 32 |
| L14-7128 | Inspections for GWB Cover | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 31 |
| L15-7128 | Inspections for GWB Cover | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 33 |

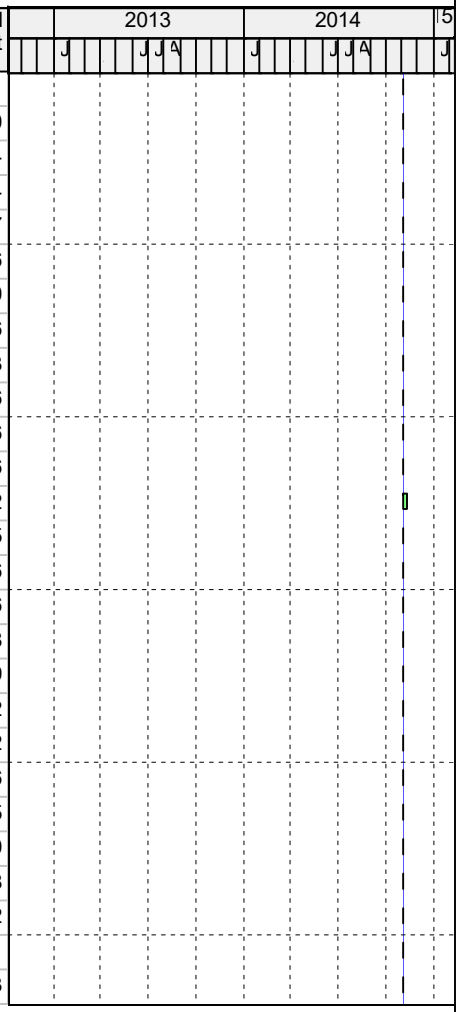



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-7128 | Inspections for GWB Cover | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 34 |
| L17-7128 | Inspections for GWB Cover | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 34 |
| L14-8136 | Bathrooms - Install Counter Subtops | 4 | 4 | 03-Nov-14 | 06-Nov-14 | 24 |
| L15-8136 | Bathrooms - Install Counter Subtops | 4 | 4 | 03-Nov-14 | 06-Nov-14 | 24 |
| LL1-Z2-8102a | GWB Hang (Ceilings) & Inspection | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 12 |
| L1K-8102a | GWB Hang (Ceilings at Public Restroom) & Inspectio | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 10 |
| L02-6016a | L2 - Electrical Room Buildout | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 41 |
| L02-8104a | L2 - Int Painting - South Half | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 27 |
| SW-2104 | Zone 1 - Install lighting conduit at SE corner | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 26 |
| SW-2110 | Zone 1 - Adjust utilities structures | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 31 |
| SW-2109 | Zone 1 - Install irrigation sleeves | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 31 |
| SW-2203 | Zone 2 - Install irrigation sleeves | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 30 |
| MPT-1024 | Tower - Caulking, east | 20 | 20 | 03-Nov-14 | 02-Dec-14 | 24 |
| MPT-1030 | Tower - Install sign backing NE (Elev 44) | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 50 |
| CO-7162 | Generator - Load bank testing | 1 | 1 | 03-Nov-14 | 03-Nov-14 | 13 |
| CO-7206 | Cx - Purge/Prove Gas-Fed Equipment and Feeder Li | 7 | 7 | 03-Nov-14 | 11-Nov-14 | 15 |
| CO-7130 | Fire Alarm - Point-To-Point Wiring | 18 | 18 | 03-Nov-14* | 26-Nov-14 | 7 |
| LL2-2086 | LL2 - Epoxy Flooring at Laundry Room | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 35 |
| L12-8216 | Vinyl Wall Coverings - Install Murals | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 40 |
| L04-8140 | Install window sills | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 26 |
| L03-8140x | Install window sills | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 41 |
| L06-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 19 |
| L03-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 40 |
| L04-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 44 |
| CO-7202 | Cx - Electrical Internal Bus & LL2-L17 Bus Duct Ener | 0 | 0 | | 03-Nov-14 A | |
| L03-8404 | GWB Hang/Tape Finish at Elevator Lobby | 5 | 5 | 04-Nov-14 | 10-Nov-14 | 8 |
| L04-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 04-Nov-14 | 10-Nov-14 | 16 |

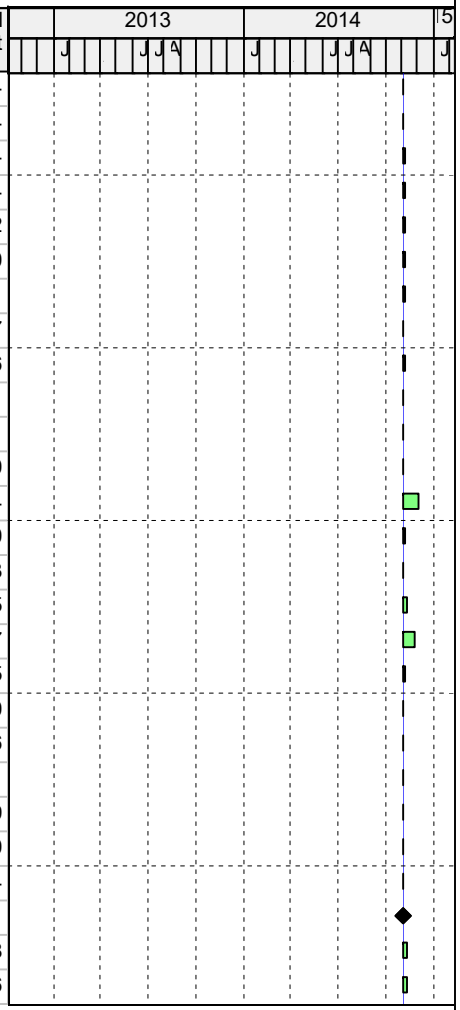


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 04-Nov-14 | 07-Nov-14 | 17 |
| L03-7130 | GWB Hang/Tape/Finish | 5 | 5 | 04-Nov-14 | 10-Nov-14 | 16 |
| L04-7130 | GWB Hang/Tape/Finish | 5 | 5 | 04-Nov-14 | 10-Nov-14 | 18 |
| LL4-8102a | LL4 - GWB Tape/Finish | 3 | 3 | 04-Nov-14 | 06-Nov-14 | 31 |
| LL3-8102a | LL3 - GWB Tape/Finish | 3 | 3 | 04-Nov-14 | 06-Nov-14 | 31 |
| SW-2210 | Zone 2 - Fine grade for sidewalk | 3 | 3 | 04-Nov-14 | 06-Nov-14 | 30 |
| CO-7164 | Generator - Final electrical inspection | 1 | 1 | 04-Nov-14 | 04-Nov-14 | 13 |
| CO-7208 | Cx - Start-Up Pumps | 3 | 3 | 04-Nov-14 | 06-Nov-14 | 0 |
| CO-7210 | Cx - Start-Up VFD's | 3 | 3 | 04-Nov-14 | 06-Nov-14 | 0 |
| L07-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 04-Nov-14 | 05-Nov-14 | 18 |
| CO-7126 | Fire pump test pre-planning complete (see checklist) | 0 | 0 | | 04-Nov-14 | 14 |
| L03-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 05-Nov-14 | 10-Nov-14 | 40 |
| L03-7030 | Paint | 1 | 1 | 05-Nov-14 | 05-Nov-14 | 25 |
| L03-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 05-Nov-14 | 10-Nov-14 | 40 |
| L05-8216 | Vinyl Wall Coverings - Install Murals | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 26 |
| SW-2214 | Zone 2 - Adjust utilities structures | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 33 |
| RF-4046 | Tower Roof - Install sheet metal capping | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 31 |
| CO-7128 | Run fire pump test | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 14 |
| CO-7160 | Generator - Cx generator/owner training | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 57 |
| L08-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 17 |
| L06-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 42 |
| L05-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 42 |
| L03-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 42 |
| L04-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 21 |
| L1BOH2-8215 | GWB Tape (Walls) | 5 | 5 | 06-Nov-14 | 12-Nov-14 | 10 |
| L03-7032 | Install VCT Flooring (x42) | 1 | 1 | 06-Nov-14 | 06-Nov-14 | 38 |
| L04-7030 | Paint | 1 | 1 | 06-Nov-14 | 06-Nov-14 | 25 |

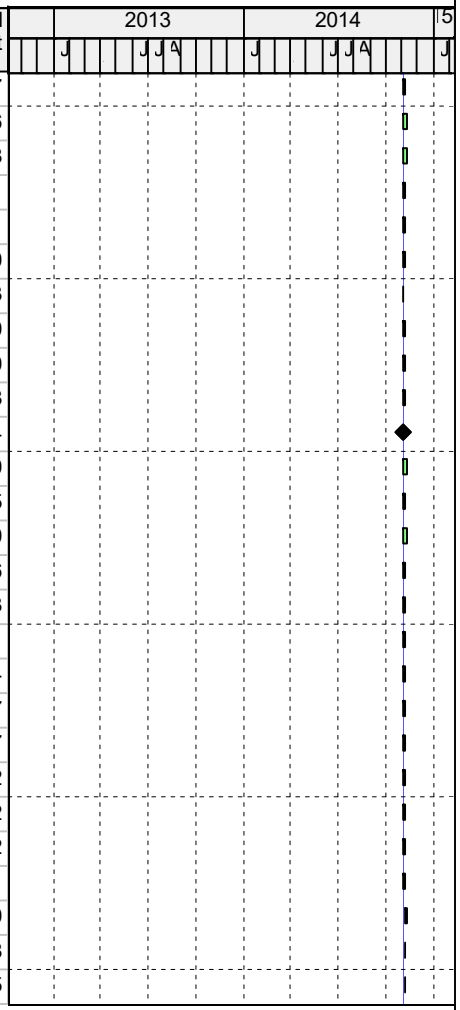



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2060 | LL2 - Paint Laundry Room | 3 | 3 | 06-Nov-14 | 10-Nov-14 | 35 |
| MPT-1032 | Tower - Install sign backing NW (Elev 51,52) | 4 | 4 | 06-Nov-14 | 11-Nov-14 | 50 |
| CO-7214 | Cx - Flush & Fill HVAC Hydronics Systems | 7 | 7 | 06-Nov-14 | 14-Nov-14 | 0 |
| L05-8140 | Install window sills | 2 | 2 | 06-Nov-14 | 07-Nov-14 | 25 |
| L09-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 06-Nov-14 | 07-Nov-14 | 16 |
| L07-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 06-Nov-14 | 07-Nov-14 | 41 |
| L05-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 07-Nov-14 | 13-Nov-14 | 8 |
| L06-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 07-Nov-14 | 13-Nov-14 | 17 |
| L04-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 07-Nov-14 | 12-Nov-14 | 38 |
| L03-7034 | Install Door and Hardware (x42) | 1 | 1 | 07-Nov-14 | 07-Nov-14 | 38 |
| L04-7032 | Install VCT Flooring (x42) | 1 | 1 | 07-Nov-14 | 07-Nov-14 | 37 |
| L05-7030 | Paint | 1 | 1 | 07-Nov-14 | 07-Nov-14 | 25 |
| L05-7130 | GWB Hang/Tape/Finish | 5 | 5 | 07-Nov-14 | 13-Nov-14 | 16 |
| L06-7130 | GWB Hang/Tape/Finish | 5 | 5 | 07-Nov-14 | 13-Nov-14 | 19 |
| L04-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 07-Nov-14 | 12-Nov-14 | 38 |
| L06-8216 | Vinyl Wall Coverings - Install Murals | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 26 |
| L12-8130 | Install Door Hardware | 3 | 3 | 07-Nov-14 | 11-Nov-14 | 39 |
| L10-8130 | Install Door Hardware | 3 | 3 | 07-Nov-14 | 11-Nov-14 | 39 |
| L12-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 24 |
| L11-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 23 |
| L10-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 15 |
| L08-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 40 |
| L06-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 19 |
| L05-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 19 |
| L03-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 40 |
| LL2E-8342 | LL2 - Final connections at walk-in cooler/freezer | 5 | 5 | 10-Nov-14 | 14-Nov-14 | 47 |
| LL1-6014Ib | L1 bar redesign - rework ceiling framing & inspection | 5 | 5 | 10-Nov-14 | 14-Nov-14 | 3 |

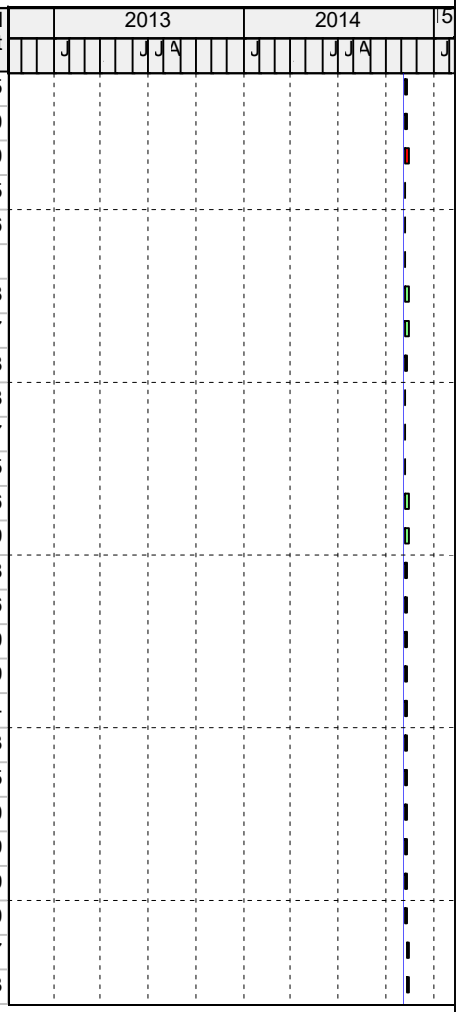


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPP-1004 | Podium - Pool Area & Cornice | 5 | 5 | 10-Nov-14 | 14-Nov-14 | 32 |
| MPP-1006 | Podium - Install Level 3 Cornice (All 4 Sides) | 5 | 5 | 10-Nov-14 | 14-Nov-14 | 32 |
| MPT-1012 | Tower - Install N/S Wing, S. End Concrete (Elev 33,3 | 10 | 10 | 10-Nov-14 | 21-Nov-14 | 42 |
| L11-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 10-Nov-14 | 13-Nov-14 | 17 |
| L16-8201 | Corridors - Install ACT Grid | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 22 |
| L03-7042 | Install Tile Flooring (x41) | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 38 |
| L04-7034 | Install Door and Hardware (x42) | 1 | 1 | 10-Nov-14 | 10-Nov-14 | 37 |
| L05-7032 | Install VCT Flooring (x42) | 1 | 1 | 10-Nov-14 | 10-Nov-14 | 39 |
| L06-7030 | Paint | 1 | 1 | 10-Nov-14 | 10-Nov-14 | 25 |
| SW-2310 | Zone 3 - Install irrigation sleeves | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 26 |
| MPT-1026 | Tower - Caulking, north | 20 | 20 | 10-Nov-14 | 09-Dec-14 | 24 |
| LL4-8116 | LL4 - Install ACT grid | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 31 |
| LL3-8116 | LL3 - Install ACT grid | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 31 |
| L16-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 6 |
| L16-8106 | Paint - Accent Walls | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 6 |
| L08-8140 | Install window sills | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 29 |
| L06-8140 | Install window sills | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 25 |
| L09-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 39 |
| L07-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 18 |
| L03-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 11-Nov-14 | 13-Nov-14 | 25 |
| L04-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 11-Nov-14 | 13-Nov-14 | 16 |
| LL2-2048 | LL2 - Set Laundry Room equipment (BY OTHERS) | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 35 |
| L03-7132 | Paint Prime/1st Coat | 3 | 3 | 11-Nov-14 | 13-Nov-14 | 32 |
| L04-7042 | Install Tile Flooring (x41) | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 37 |
| L05-7034 | Install Door and Hardware (x42) | 1 | 1 | 11-Nov-14 | 11-Nov-14 | 39 |
| L06-7032 | Install VCT Flooring (x42) | 1 | 1 | 11-Nov-14 | 11-Nov-14 | 35 |
| L07-7030 | Paint | 1 | 1 | 11-Nov-14 | 11-Nov-14 | 25 |

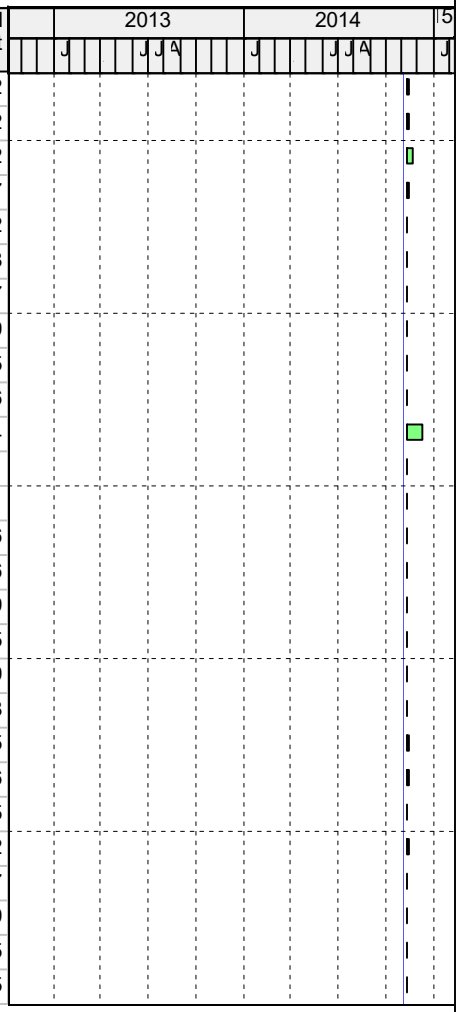



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7132 | Paint Prime/1st Coat | 3 | 3 | 11-Nov-14 | 13-Nov-14 | 18 |
| L07-8216 | Vinyl Wall Coverings - Install Murals | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 26 |
| SW-2212 | Zone 2 - FRP sidewalk | 3 | 3 | 11-Nov-14 | 13-Nov-14 | 28 |
| SW-2312 | Zone 3 - Fine grade for sidewalk (excl. manlift area) | 3 | 3 | 11-Nov-14 | 13-Nov-14 | 26 |
| RF-4042 | Pool Roof - Install metal coping at high roof | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 31 |
| L07-8140 | Install window sills | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 26 |
| L12-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 38 |
| L11-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 38 |
| L10-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 38 |
| L08-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 17 |
| L1BOH2-8104 | Prime Paint | 4 | 4 | 12-Nov-14 | 15-Nov-14 | 12 |
| L07-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 8 |
| L08-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 18 |
| L03-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 12-Nov-14 | 12-Nov-14 | 38 |
| L05-7042 | Install Tile Flooring (x41) | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 39 |
| L06-7034 | Install Door and Hardware (x42) | 1 | 1 | 12-Nov-14 | 12-Nov-14 | 35 |
| L07-7032 | Install VCT Flooring (x42) | 1 | 1 | 12-Nov-14 | 12-Nov-14 | 34 |
| L08-7030 | Paint | 1 | 1 | 12-Nov-14 | 12-Nov-14 | 25 |
| L07-7130 | GWB Hang/Tape/Finish | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 16 |
| L08-7130 | GWB Hang/Tape/Finish | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 20 |
| L16-8136 | Bathrooms - Install Counter Subtops | 4 | 4 | 12-Nov-14 | 17-Nov-14 | 20 |
| L02-8130 | L2 - Install ACT Grid | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 22 |
| SW-2118 | Zone 1 - FRP sidewalk | 3 | 3 | 12-Nov-14 | 14-Nov-14 | 27 |
| CO-7212 | Cx - Start-Up Boilers | 3 | 3 | 12-Nov-14 | 14-Nov-14 | 15 |
| LL1-Z2-8115 | Install MEP Drops To T Bar Grid Ceiling | 3 | 3 | 12-Nov-14 | 14-Nov-14 | 12 |
| L16-8111 | Paint - Door Jambs | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 19 |
| L09-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 16 |

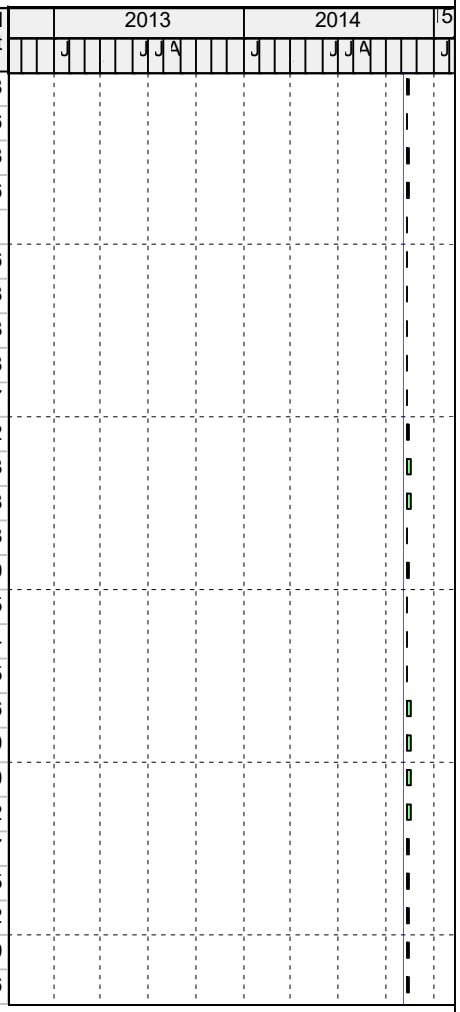



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2050 | LL2 - Laundry Room equipment final connections (MI | 1 | 1 | 13-Nov-14 | 13-Nov-14 | 35 |
| L04-7044 | Install Vending Cabinets (x41) | 1 | 1 | 13-Nov-14 | 13-Nov-14 | 37 |
| L06-7042 | Install Tile Flooring (x41) | 2 | 2 | 13-Nov-14 | 14-Nov-14 | 35 |
| L07-7034 | Install Door and Hardware (x42) | 1 | 1 | 13-Nov-14 | 13-Nov-14 | 34 |
| L08-7032 | Install VCT Flooring (x42) | 1 | 1 | 13-Nov-14 | 13-Nov-14 | 33 |
| L09-7030 | Paint | 1 | 1 | 13-Nov-14 | 13-Nov-14 | 25 |
| LL2-2062 | LL2 - Install ceiling grid | 2 | 2 | 13-Nov-14 | 14-Nov-14 | 35 |
| L08-8216 | Vinyl Wall Coverings - Install Murals | 2 | 2 | 13-Nov-14 | 14-Nov-14 | 26 |
| SW-2314 | Zone 3 - FRP sidewalk (excl. manlift area) | 3 | 3 | 13-Nov-14 | 17-Nov-14 | 26 |
| RF-4040 | L2.5 Horseshoe - Install sheet metal capping | 3 | 3 | 13-Nov-14 | 17-Nov-14 | 31 |
| L14-8130 | Install Door Hardware | 3 | 3 | 13-Nov-14 | 17-Nov-14 | 35 |
| L09-8140 | Install window sills | 2 | 2 | 13-Nov-14 | 14-Nov-14 | 28 |
| L12-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 13-Nov-14 | 14-Nov-14 | 24 |
| L11-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 13-Nov-14 | 14-Nov-14 | 23 |
| L10-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 13-Nov-14 | 14-Nov-14 | 15 |
| L03-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 14-Nov-14 | 17-Nov-14 | 25 |
| L04-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 14-Nov-14 | 17-Nov-14 | 16 |
| L05-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 14-Nov-14 | 18-Nov-14 | 15 |
| L06-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 14-Nov-14 | 18-Nov-14 | 17 |
| L1K-8340 | Install walk-in cooler/freezer (BY OTHERS) | 2 | 2 | 14-Nov-14 | 17-Nov-14 | 9 |
| L05-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 14-Nov-14 | 19-Nov-14 | 33 |
| L12-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 14-Nov-14 | 19-Nov-14 | 17 |
| L05-7044 | Install Vending Cabinets (x41) | 1 | 1 | 14-Nov-14 | 14-Nov-14 | 41 |
| L07-7042 | Install Tile Flooring (x41) | 2 | 2 | 14-Nov-14 | 17-Nov-14 | 34 |
| L08-7034 | Install Door and Hardware (x42) | 1 | 1 | 14-Nov-14 | 14-Nov-14 | 33 |
| L09-7032 | Install VCT Flooring (x42) | 1 | 1 | 14-Nov-14 | 14-Nov-14 | 32 |
| L10-7030 | Paint | 1 | 1 | 14-Nov-14 | 14-Nov-14 | 25 |

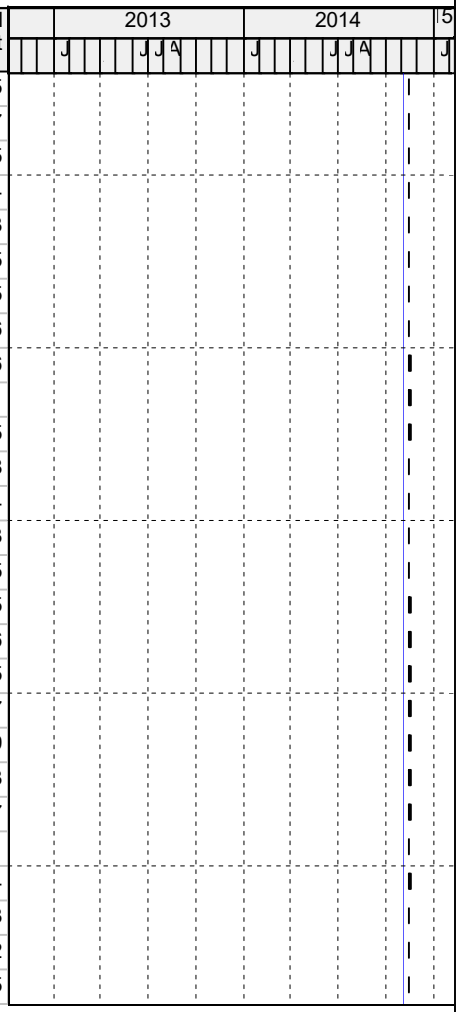



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7132 | Paint Prime/1st Coat | 3 | 3 | 14-Nov-14 | 18-Nov-14 | 17 |
| L06-7132 | Paint Prime/1st Coat | 3 | 3 | 14-Nov-14 | 18-Nov-14 | 19 |
| L05-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 14-Nov-14 | 19-Nov-14 | 33 |
| SW-2216 | Zone 2 - Install irrigation | 10 | 10 | 14-Nov-14 | 01-Dec-14 | 43 |
| SW-2218 | Zone 2 - Install landscaping | 10 | 10 | 14-Nov-14 | 01-Dec-14 | 43 |
| RF-4050 | Roof at Manlift - Erect steel | 1 | 1 | 14-Nov-14 | 14-Nov-14 | 40 |
| CO-7216 | Cx - Glycol Add/Circulate | 3 | 3 | 14-Nov-14 | 18-Nov-14 | 0 |
| LL1-8120 | Install MEP Drops To T Bar Grid Ceiling | 3 | 3 | 14-Nov-14 | 18-Nov-14 | 8 |
| LL1-Z3-8115 | Install MEP Drops To T Bar Grid Ceiling | 3 | 3 | 14-Nov-14 | 18-Nov-14 | 11 |
| L14-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 14-Nov-14 | 17-Nov-14 | 20 |
| L1BOH2-8114 | T Bar Grid Ceiling | 3 | 3 | 17-Nov-14 | 19-Nov-14 | 10 |
| I-1602 | Enclosure at manlift - Install air barrier | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 15 |
| L09-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 8 |
| L10-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 17 |
| L1K-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 17-Nov-14 | 18-Nov-14 | 9 |
| L17-8201 | Corridors - Install ACT Grid | 2 | 2 | 17-Nov-14 | 18-Nov-14 | 18 |
| L06-7044 | Install Vending Cabinets (x41) | 1 | 1 | 17-Nov-14 | 17-Nov-14 | 35 |
| L08-7042 | Install Tile Flooring (x41) | 2 | 2 | 17-Nov-14 | 18-Nov-14 | 33 |
| L09-7034 | Install Door and Hardware (x42) | 1 | 1 | 17-Nov-14 | 17-Nov-14 | 32 |
| L10-7032 | Install VCT Flooring (x42) | 1 | 1 | 17-Nov-14 | 17-Nov-14 | 31 |
| L11-7030 | Paint | 1 | 1 | 17-Nov-14 | 17-Nov-14 | 25 |
| L09-7130 | GWB Hang/Tape/Finish | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 16 |
| L10-7130 | GWB Hang/Tape/Finish | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 21 |
| LL1-6014Ib2 | L1 bar redesign - GWB hang at ceilings | 4 | 4 | 17-Nov-14 | 20-Nov-14 | 3 |
| MPT-1018a | Tower - Install Roof Cornice Metal | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 42 |
| SW-2120 | Zone 1 - Install irrigation | 10 | 10 | 17-Nov-14 | 02-Dec-14 | 42 |
| SW-2122 | Zone 1 - Install landscaping | 10 | 10 | 17-Nov-14 | 02-Dec-14 | 42 |

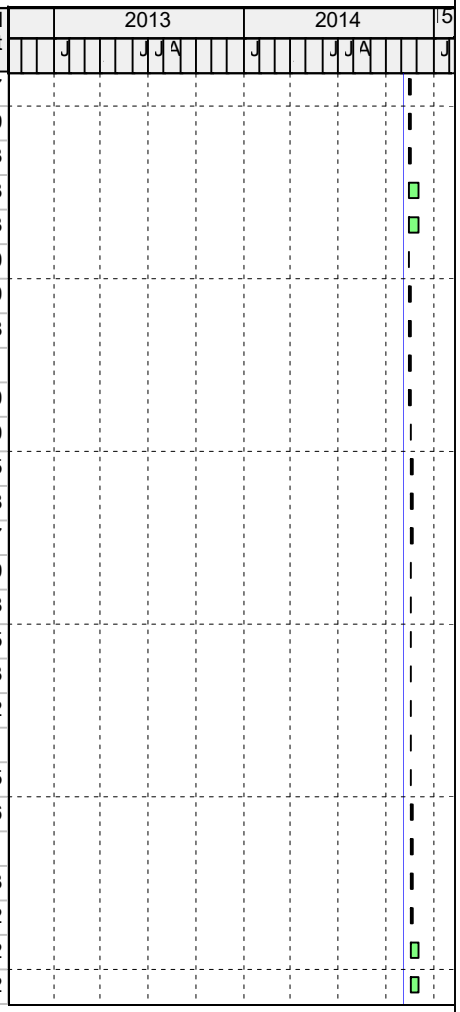



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2316 | Zone 3 - Demolish manlift shack and base | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 34 |
| RF-4052 | Roof at Manlift - Framing/sheathing/air barrier (inspec | 4 | 4 | 17-Nov-14 | 20-Nov-14 | 32 |
| RF-4064 | Pool Green Roof - Install sheet metal capping | 3 | 3 | 17-Nov-14 | 19-Nov-14 | 31 |
| MPP-1012 | Podium - Caulking, south | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 32 |
| LL2-2088 | LL2 - Install MEP Drops to Grid | 3 | 3 | 17-Nov-14 | 19-Nov-14 | 35 |
| L17-8106 | Paint - Accent Walls | 2 | 2 | 17-Nov-14 | 18-Nov-14 | 5 |
| L17-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 2 | 17-Nov-14 | 18-Nov-14 | 5 |
| L11-8130 | Install Door Hardware | 3 | 3 | 17-Nov-14 | 19-Nov-14 | 33 |
| L10-8140 | Install window sills | 2 | 2 | 17-Nov-14 | 18-Nov-14 | 28 |
| L09-8216 | Vinyl Wall Coverings - Install Murals | 2 | 2 | 17-Nov-14 | 18-Nov-14 | 26 |
| L03-8648 | Pool- Install pool deck waterproofing | 4 | 4 | 17-Nov-14 | 20-Nov-14 | 14 |
| L03-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 18-Nov-14 | 20-Nov-14 | 25 |
| L03-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 18-Nov-14 | 18-Nov-14 | 27 |
| L04-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 18-Nov-14 | 20-Nov-14 | 16 |
| L04-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 18-Nov-14 | 18-Nov-14 | 18 |
| L06-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 18-Nov-14 | 21-Nov-14 | 31 |
| L03-7138 | Electrical Trim-Out | 2 | 2 | 18-Nov-14 | 19-Nov-14 | 30 |
| L03-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 18-Nov-14 | 20-Nov-14 | 30 |
| L07-7044 | Install Vending Cabinets (x41) | 1 | 1 | 18-Nov-14 | 18-Nov-14 | 34 |
| L09-7042 | Install Tile Flooring (x41) | 2 | 2 | 18-Nov-14 | 19-Nov-14 | 32 |
| L10-7034 | Install Door and Hardware (x42) | 1 | 1 | 18-Nov-14 | 18-Nov-14 | 31 |
| L11-7032 | Install VCT Flooring (x42) | 1 | 1 | 18-Nov-14 | 18-Nov-14 | 30 |
| L12-7030 | Paint | 1 | 1 | 18-Nov-14 | 18-Nov-14 | 25 |
| L04-7138 | Electrical Trim-Out | 2 | 2 | 18-Nov-14 | 19-Nov-14 | 16 |
| L04-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 18-Nov-14 | 20-Nov-14 | 16 |
| L06-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 18-Nov-14 | 21-Nov-14 | 31 |
| L1B-8102a | GWB Hang (Ceilings) | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 9 |

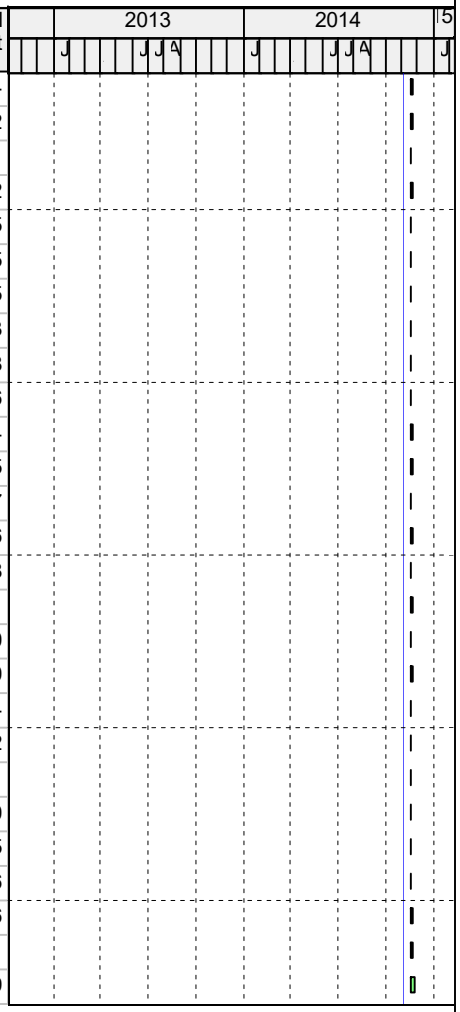



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-7144 | Fire Sprinkler Trim | 1 | 1 | 18-Nov-14 | 18-Nov-14 | 32 |
| L04-7144 | Fire Sprinkler Trim | 1 | 1 | 18-Nov-14 | 18-Nov-14 | 18 |
| RF-4072 | Pool Roof - Install metal coping | 3 | 3 | 18-Nov-14 | 20-Nov-14 | 41 |
| L16-8216 | Vinyl Wall Coverings - Install Murals | 2 | 2 | 18-Nov-14 | 19-Nov-14 | 10 |
| L14-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 18-Nov-14 | 19-Nov-14 | 33 |
| L05-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 19-Nov-14 | 20-Nov-14 | 15 |
| L06-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 19-Nov-14 | 20-Nov-14 | 17 |
| L07-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 19-Nov-14 | 21-Nov-14 | 16 |
| L08-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 19-Nov-14 | 21-Nov-14 | 18 |
| CO-7100T | Cx - Equipment Start-Up & Testing, Tower | 10 | 10 | 19-Nov-14 | 04-Dec-14 | 3 |
| L07-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 19-Nov-14 | 24-Nov-14 | 30 |
| L08-7044 | Install Vending Cabinets (x41) | 1 | 1 | 19-Nov-14 | 19-Nov-14 | 33 |
| L10-7042 | Install Tile Flooring (x41) | 2 | 2 | 19-Nov-14 | 20-Nov-14 | 31 |
| L11-7034 | Install Door and Hardware (x42) | 1 | 1 | 19-Nov-14 | 19-Nov-14 | 30 |
| L12-7032 | Install VCT Flooring (x42) | 1 | 1 | 19-Nov-14 | 19-Nov-14 | 29 |
| L14-7030 | Paint | 1 | 1 | 19-Nov-14 | 19-Nov-14 | 25 |
| L07-7132 | Paint Prime/1st Coat | 3 | 3 | 19-Nov-14 | 21-Nov-14 | 18 |
| L08-7132 | Paint Prime/1st Coat | 3 | 3 | 19-Nov-14 | 21-Nov-14 | 20 |
| L07-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 19-Nov-14 | 24-Nov-14 | 30 |
| L17-8136 | Bathrooms - Install Counter Subtops | 4 | 4 | 19-Nov-14 | 24-Nov-14 | 15 |
| MPP-1016 | Podium - Caulking, east | 6 | 6 | 19-Nov-14 | 26-Nov-14 | 34 |
| MPT-1040 | Tower - Install N/S Wing, S, End (Elev 30) | 6 | 6 | 19-Nov-14 | 26-Nov-14 | 15 |
| CO-7400 | Cx - 3rd Party Cx of Mechanical, Plumbing, Electrical | 40 | 40 | 19-Nov-14 | 20-Jan-15 | 0 |
| CO-7218 | Cx - Start-Up & Test Hydronics System, Tower | 10 | 10 | 19-Nov-14 | 04-Dec-14 | 40 |
| CO-7220 | Cx - Start-Up & Test Hydronics System, Podium | 18 | 18 | 19-Nov-14 | 16-Dec-14 | 0 |
| L17-8111 | Paint - Door Jambs | 2 | 2 | 19-Nov-14 | 20-Nov-14 | 16 |
| L1BOH2C-6024 | MEP Trim at Ceiling | 3 | 3 | 19-Nov-14 | 21-Nov-14 | 10 |

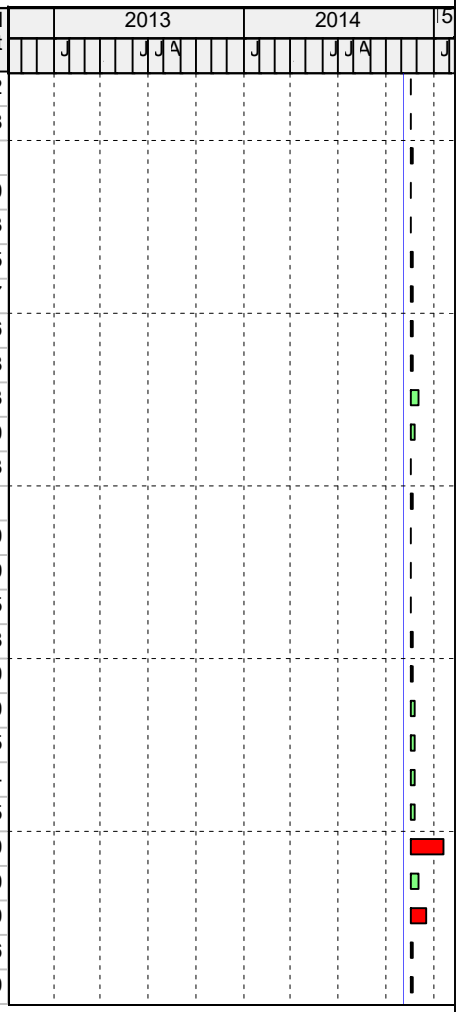



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8216 | Vinyl Wall Coverings - Install Murals | 2 | 2 | 19-Nov-14 | 20-Nov-14 | 26 |
| L1BOH2-8140 | Acoustical Ceiling Tile | 2 | 2 | 20-Nov-14 | 21-Nov-14 | 10 |
| L04-8418 | Flooring at Elevator Lobby | 3 | 3 | 20-Nov-14 | 24-Nov-14 | 26 |
| L11-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 8 |
| L12-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 14 |
| L08-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 20-Nov-14 | 25-Nov-14 | 29 |
| L14-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 20-Nov-14 | 25-Nov-14 | 17 |
| L09-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 20-Nov-14 | 20-Nov-14 | 32 |
| L11-7042 | Install Tile Flooring (x41) | 2 | 2 | 20-Nov-14 | 21-Nov-14 | 30 |
| L12-7034 | Install Door and Hardware (x42) | 1 | 1 | 20-Nov-14 | 20-Nov-14 | 29 |
| L14-7032 | Install VCT Flooring (x42) | 1 | 1 | 20-Nov-14 | 20-Nov-14 | 28 |
| L15-7030 | Paint | 1 | 1 | 20-Nov-14 | 20-Nov-14 | 25 |
| L11-7130 | GWB Hang/Tape/Finish | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 16 |
| L12-7130 | GWB Hang/Tape/Finish | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 20 |
| L08-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 20-Nov-14 | 25-Nov-14 | 29 |
| PC-4012 | Porte Cochere - Install sheet metal capping | 3 | 3 | 20-Nov-14 | 24-Nov-14 | 41 |
| LL2-2090 | LL2 - Install ceiling tile | 1 | 1 | 20-Nov-14 | 20-Nov-14 | 35 |
| LL2-2092 | LL2 - MEP trim | 3 | 3 | 20-Nov-14 | 24-Nov-14 | 35 |
| L15-8130 | Install Door Hardware | 3 | 3 | 20-Nov-14 | 24-Nov-14 | 30 |
| L11-8140 | Install window sills | 2 | 2 | 20-Nov-14 | 21-Nov-14 | 27 |
| L14-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 20-Nov-14 | 21-Nov-14 | 20 |
| L03-8418 | Flooring at Elevator Lobby | 3 | 3 | 21-Nov-14 | 25-Nov-14 | 25 |
| L05-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 21-Nov-14 | 25-Nov-14 | 15 |
| L05-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 21-Nov-14 | 21-Nov-14 | 17 |
| L06-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 21-Nov-14 | 25-Nov-14 | 17 |
| L06-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 21-Nov-14 | 21-Nov-14 | 19 |
| L10-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 21-Nov-14 | 21-Nov-14 | 31 |

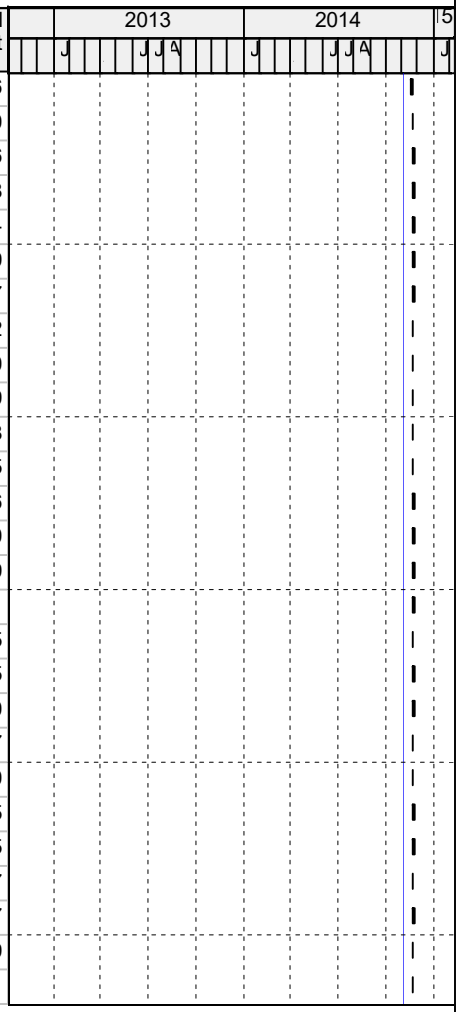



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7042 | Install Tile Flooring (x41) | 2 | 2 | 21-Nov-14 | 24-Nov-14 | 29 |
| L14-7034 | Install Door and Hardware (x42) | 1 | 1 | 21-Nov-14 | 21-Nov-14 | 28 |
| L15-7032 | Install VCT Flooring (x42) | 1 | 1 | 21-Nov-14 | 21-Nov-14 | 27 |
| L16-7030 | Paint | 1 | 1 | 21-Nov-14 | 21-Nov-14 | 25 |
| L05-7138 | Electrical Trim-Out | 2 | 2 | 21-Nov-14 | 24-Nov-14 | 15 |
| L05-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 21-Nov-14 | 25-Nov-14 | 15 |
| L06-7138 | Electrical Trim-Out | 2 | 2 | 21-Nov-14 | 24-Nov-14 | 17 |
| L06-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 21-Nov-14 | 25-Nov-14 | 17 |
| LL1-Z2-8124a | Install Base | 3 | 3 | 21-Nov-14 | 25-Nov-14 | 12 |
| L05-7144 | Fire Sprinkler Trim | 1 | 1 | 21-Nov-14 | 21-Nov-14 | 17 |
| L06-7144 | Fire Sprinkler Trim | 1 | 1 | 21-Nov-14 | 21-Nov-14 | 19 |
| RF-4054 | Roof at Manlift - Final mechanical installations | 4 | 4 | 21-Nov-14 | 26-Nov-14 | 32 |
| LL1-6014Id | L1 bar redesign - Complete finishes at ceilings | 5 | 5 | 21-Nov-14 | 01-Dec-14 | 3 |
| L11-8216 | Vinyl Wall Coverings - Install Murals | 2 | 2 | 21-Nov-14 | 24-Nov-14 | 26 |
| L1BOH2-8200 | First Coat Finish Paint | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 10 |
| L07-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 16 |
| L08-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 18 |
| L09-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 17 |
| L10-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 17 |
| L11-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 24-Nov-14 | 24-Nov-14 | 30 |
| L14-7042 | Install Tile Flooring (x41) | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 28 |
| L15-7034 | Install Door and Hardware (x42) | 1 | 1 | 24-Nov-14 | 24-Nov-14 | 27 |
| L16-7032 | Install VCT Flooring (x42) | 1 | 1 | 24-Nov-14 | 24-Nov-14 | 27 |
| L17-7030 | Paint | 1 | 1 | 24-Nov-14 | 24-Nov-14 | 25 |
| L09-7132 | Paint Prime/1st Coat | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 19 |
| L10-7132 | Paint Prime/1st Coat | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 21 |
| L03-8638 | Pool - Install pool deck and ADA lift | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 13 |

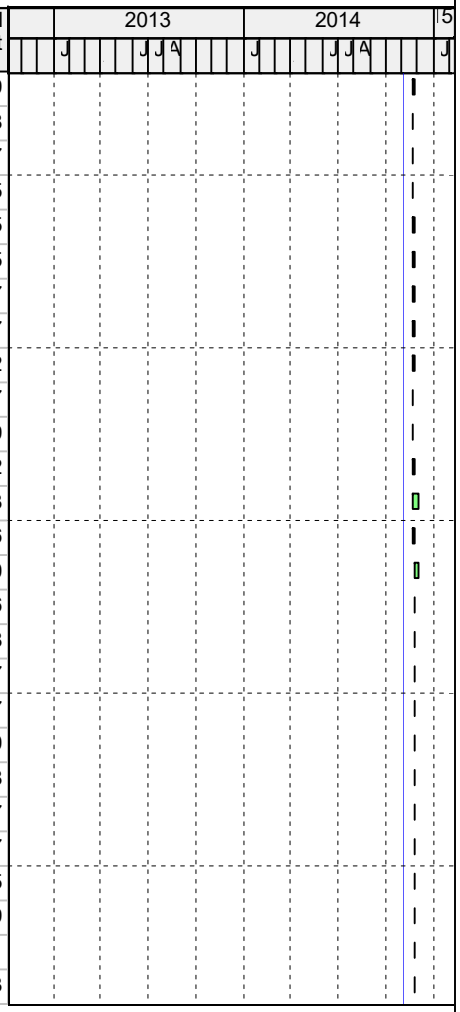



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2318 | Zone 3 - Fine grade for sidewalk at manlift | 1 | 1 | 24-Nov-14 | 24-Nov-14 | 34 |
| MPP-1014 | Podium - Caulking, west | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 32 |
| MPT-1042 | Enclosure at manlift - air barrier & Insulation | 7 | 7 | 24-Nov-14 | 04-Dec-14 | 15 |
| LL1-Z3-8142 | Install Restroom Ceramic Tile | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 26 |
| L12-8140 | Install window sills | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 25 |
| L04-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 25-Nov-14 | 26-Nov-14 | 26 |
| L14-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 25-Nov-14 | 03-Dec-14 | 8 |
| L15-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 25-Nov-14 | 03-Dec-14 | 11 |
| L09-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 33 |
| L12-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 25-Nov-14 | 25-Nov-14 | 29 |
| L15-7042 | Install Tile Flooring (x41) | 2 | 2 | 25-Nov-14 | 26-Nov-14 | 27 |
| L16-7034 | Install Door and Hardware (x42) | 1 | 1 | 25-Nov-14 | 25-Nov-14 | 27 |
| L17-7032 | Install VCT Flooring (x42) | 1 | 1 | 25-Nov-14 | 25-Nov-14 | 25 |
| L14-7130 | GWB Hang/Tape/Finish | 5 | 5 | 25-Nov-14 | 03-Dec-14 | 16 |
| L15-7130 | GWB Hang/Tape/Finish | 5 | 5 | 25-Nov-14 | 03-Dec-14 | 18 |
| L09-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 26 |
| SW-2320 | Zone 3 - FRP sidewalk at manlift | 2 | 2 | 25-Nov-14 | 26-Nov-14 | 34 |
| RF-4056 | Roof at Manlift - Final electrical connections | 2 | 2 | 25-Nov-14 | 26-Nov-14 | 32 |
| LL2-2094 | LL2 - Install doors & hardware | 1 | 1 | 25-Nov-14 | 25-Nov-14 | 35 |
| L17-8216 | Vinyl Wall Coverings - Install Murals | 2 | 2 | 25-Nov-14 | 26-Nov-14 | 5 |
| L15-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 25-Nov-14 | 26-Nov-14 | 14 |
| L03-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 25 |
| L05-8418 | Flooring at Elevator Lobby | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 23 |
| L06-8418 | Flooring at Elevator Lobby | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 23 |
| L07-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 16 |
| L07-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 26-Nov-14 | 26-Nov-14 | 18 |
| L08-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 18 |

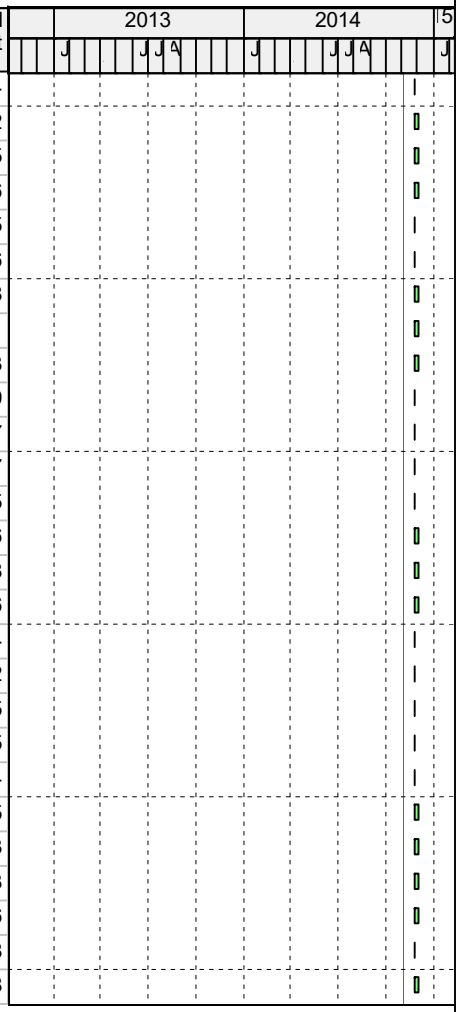



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 26-Nov-14 | 26-Nov-14 | 20 |
| CO-7102T | Cx - DDC Point-To-Point Checks, Tower | 5 | 5 | 26-Nov-14 | 04-Dec-14 | 35 |
| L15-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 26-Nov-14 | 03-Dec-14 | 17 |
| L14-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 26-Nov-14 | 26-Nov-14 | 28 |
| L16-7042 | Install Tile Flooring (x41) | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 27 |
| L17-7034 | Install Door and Hardware (x42) | 1 | 1 | 26-Nov-14 | 26-Nov-14 | 25 |
| L07-7138 | Electrical Trim-Out | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 16 |
| L07-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 16 |
| L08-7138 | Electrical Trim-Out | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 18 |
| L08-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 18 |
| L02-8138 | L2 - Install ceiling tile | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 22 |
| L07-7144 | Fire Sprinkler Trim | 1 | 1 | 26-Nov-14 | 26-Nov-14 | 18 |
| L08-7144 | Fire Sprinkler Trim | 1 | 1 | 26-Nov-14 | 26-Nov-14 | 20 |
| RF-4066 | Pool Green Roof - Install decorative metal railing | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 31 |
| L1K-8210 | Install Restroom Ceramic Tile | 5 | 5 | 26-Nov-14 | 04-Dec-14 | 23 |
| L04-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 26 |
| L09-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 17 |
| L10-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 17 |
| L11-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 14 |
| L12-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 14 |
| LL1-Z3-8340 | Install walk-in cooler/freezer (BY OTHERS) | 5 | 5 | 01-Dec-14* | 05-Dec-14 | 28 |
| L10-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 01-Dec-14 | 04-Dec-14 | 31 |
| L15-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 01-Dec-14 | 01-Dec-14 | 27 |
| L17-7042 | Install Tile Flooring (x41) | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 25 |
| L04-7134 | Install VCT Flooring | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 12 |
| L11-7132 | Paint Prime/1st Coat | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 20 |
| L12-7132 | Paint Prime/1st Coat | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 20 |

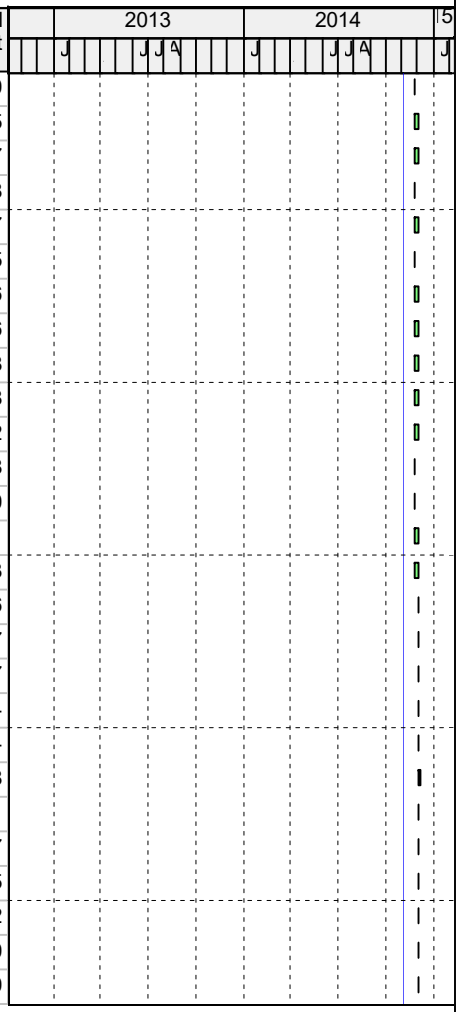



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8640 | Pool - Prep and install plaster | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 13 |
| L10-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 01-Dec-14 | 04-Dec-14 | 24 |
| L1L-8102a | GWB Hang/Tape (Ceilings) | 11 | 11 | 01-Dec-14 | 15-Dec-14 | 1 |
| SW-2322 | Zone 3 - Install irrigation | 10 | 10 | 01-Dec-14 | 12-Dec-14 | 34 |
| SW-2324 | Zone 3 - Install landscaping | 10 | 10 | 01-Dec-14 | 12-Dec-14 | 34 |
| RF-4058 | Roof at Manlift - Install roofing | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 32 |
| L15-8140 | Install window sills | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 23 |
| L14-8140 | Install window sills | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 23 |
| L15-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 26 |
| CM-1016a | CM - Owner FF+E "Build-Out" - Floors 3, 11-17 | 17 | 17 | 01-Dec-14 | 17-Dec-14 | 22 |
| L03-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 25 |
| L05-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 23 |
| L06-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 23 |
| L16-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 8 |
| L17-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 8 |
| L16-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 02-Dec-14 | 02-Dec-14 | 27 |
| L16-7130 | GWB Hang/Tape/Finish | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 16 |
| L17-7130 | GWB Hang/Tape/Finish | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 16 |
| L16-8218 | Corridors - Fire Sprinkler Trim | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 10 |
| L1BOH2-8124 | Flooring | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 10 |
| L07-8418 | Flooring at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 20 |
| L08-8418 | Flooring at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 20 |
| L09-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 17 |
| L09-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 19 |
| L10-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 17 |
| L10-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 19 |
| L03-8612 | L3 Pool - GWB hang/tape/finish | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 13 |

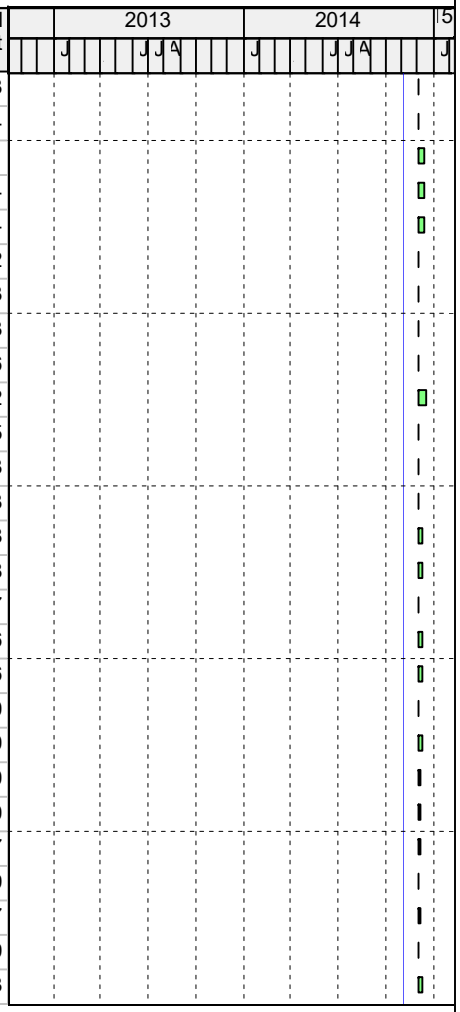



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 25 |
| L04-7136 | Install Door and Hardware | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 28 |
| L05-7134 | Install VCT Flooring | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 12 |
| L09-7138 | Electrical Trim-Out | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 17 |
| L09-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 17 |
| L10-7138 | Electrical Trim-Out | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 19 |
| L10-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 19 |
| L03-8642 | Pool - Fill pool | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 32 |
| L1K-8124a | Install Flooring (Epoxy) | 7 | 7 | 03-Dec-14 | 10-Dec-14 | 11 |
| L09-7144 | Fire Sprinkler Trim | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 19 |
| L10-7144 | Fire Sprinkler Trim | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 21 |
| RF-4060 | Roof at Manlift - Install corrugated metal panels | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 32 |
| RF-4068 | Pool Green Roof - Install American Hydrotech assem | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 31 |
| MPT-1028 | Tower - Caulking, south | 13 | 13 | 03-Dec-14 | 19-Dec-14 | 24 |
| MPP-1018 | Podium - Caulking, north | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 32 |
| LL1-Z3-8144 | Install Restroom Fixtures | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 26 |
| L16-8130 | Install Door Hardware | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 24 |
| L15-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 14 |
| L05-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 23 |
| L06-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 23 |
| L11-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 14 |
| L12-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 14 |
| L14-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 11 |
| L15-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 11 |
| L11-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 04-Dec-14 | 09-Dec-14 | 21 |
| L16-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 04-Dec-14 | 09-Dec-14 | 17 |
| L14-7132 | Paint Prime/1st Coat | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 20 |

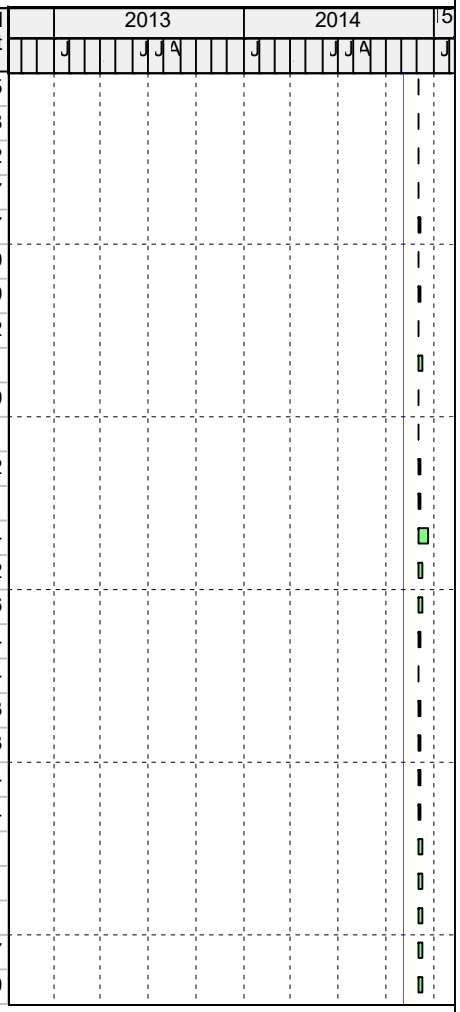



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-7132 | Paint Prime/1st Coat | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 18 |
| L11-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 04-Dec-14 | 09-Dec-14 | 21 |
| LL1-8124a | Install Base | 5 | 5 | 04-Dec-14 | 10-Dec-14 | 3 |
| L04-7146 | Final Coat Finish Paint | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 28 |
| L17-8140 | Install window sills | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 20 |
| L16-8140 | Install window sills | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 21 |
| L16-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 10 |
| L07-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 20 |
| L08-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 20 |
| CO-7110T | Fire Sprinkler Pre-Testing (Tower) | 15 | 15 | 05-Dec-14 | 29-Dec-14 | 3 |
| CO-7116T | Fire Alarm Pre-Testing (Tower) | 15 | 15 | 05-Dec-14 | 29-Dec-14 | 3 |
| CO-7104T | Smoke Control Pre-Testing (Tower) | 15 | 15 | 05-Dec-14 | 29-Dec-14 | 3 |
| L05-7136 | Install Door and Hardware | 1 | 1 | 05-Dec-14 | 05-Dec-14 | 26 |
| L06-7134 | Install VCT Flooring | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 12 |
| L03-8644 | Pool - Start-up and adjust pool equipment | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 32 |
| L1BOH2-8124a | Install Base | 3 | 3 | 05-Dec-14 | 09-Dec-14 | 11 |
| MPT-1044 | Tower - Install sign backing south | 3 | 3 | 05-Dec-14 | 09-Dec-14 | 15 |
| L1K-8206 | Install Restroom Fixtures | 5 | 5 | 05-Dec-14 | 11-Dec-14 | 23 |
| L09-8418 | Flooring at Elevator Lobby | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 17 |
| L10-8418 | Flooring at Elevator Lobby | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 17 |
| L11-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 14 |
| L11-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 08-Dec-14 | 08-Dec-14 | 16 |
| L12-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 14 |
| L12-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 08-Dec-14 | 08-Dec-14 | 16 |
| LL1-Z3-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 08-Dec-14* | 09-Dec-14 | 28 |
| L12-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 08-Dec-14 | 11-Dec-14 | 19 |
| L11-7138 | Electrical Trim-Out | 2 | 2 | 08-Dec-14 | 09-Dec-14 | 18 |

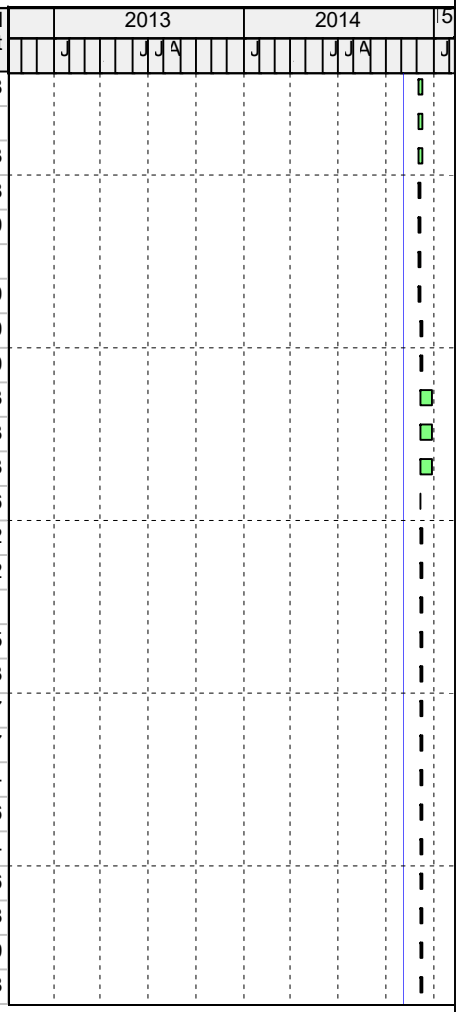



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 18 |
| L12-7138 | Electrical Trim-Out | 2 | 2 | 08-Dec-14 | 09-Dec-14 | 18 |
| L12-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 18 |
| L12-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 08-Dec-14 | 11-Dec-14 | 19 |
| L05-7146 | Final Coat Finish Paint | 2 | 2 | 08-Dec-14 | 09-Dec-14 | 26 |
| L11-7144 | Fire Sprinkler Trim | 1 | 1 | 08-Dec-14 | 08-Dec-14 | 20 |
| L12-7144 | Fire Sprinkler Trim | 1 | 1 | 08-Dec-14 | 08-Dec-14 | 20 |
| RF-4062 | Roof at Manlift - Install sheet metal capping | 2 | 2 | 08-Dec-14 | 09-Dec-14 | 32 |
| RF-4070 | TR - Terrace Roof - Install American Hydrotech assem | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 31 |
| L16-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 08-Dec-14 | 09-Dec-14 | 22 |
| L07-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 09-Dec-14 | 10-Dec-14 | 20 |
| L08-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 09-Dec-14 | 10-Dec-14 | 20 |
| L14-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 09-Dec-14 | 10-Dec-14 | 11 |
| L15-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 09-Dec-14 | 10-Dec-14 | 11 |
| L16-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 09-Dec-14 | 11-Dec-14 | 9 |
| L17-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 09-Dec-14 | 11-Dec-14 | 8 |
| L06-7136 | Install Door and Hardware | 1 | 1 | 09-Dec-14 | 09-Dec-14 | 24 |
| L07-7134 | Install VCT Flooring | 2 | 2 | 09-Dec-14 | 10-Dec-14 | 12 |
| L16-7132 | Paint Prime/1st Coat | 3 | 3 | 09-Dec-14 | 11-Dec-14 | 17 |
| L17-7132 | Paint Prime/1st Coat | 3 | 3 | 09-Dec-14 | 11-Dec-14 | 16 |
| L03-8646 | Pool - Health inspections | 1 | 1 | 09-Dec-14 | 09-Dec-14 | 32 |
| L1BOH2-8116 | Finish Carpentry / Millwork | 5 | 5 | 10-Dec-14 | 16-Dec-14 | 10 |
| L1BOH2-8126 | Doors & Hardware | 5 | 5 | 10-Dec-14 | 16-Dec-14 | 18 |
| L09-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 17 |
| L10-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 17 |
| LL1-Z2-8118a | Install decorative light fixtures | 3 | 3 | 10-Dec-14 | 12-Dec-14 | 24 |
| L03-8614 | L3 Pool - Paint/wall finishes | 3 | 3 | 10-Dec-14 | 12-Dec-14 | 15 |

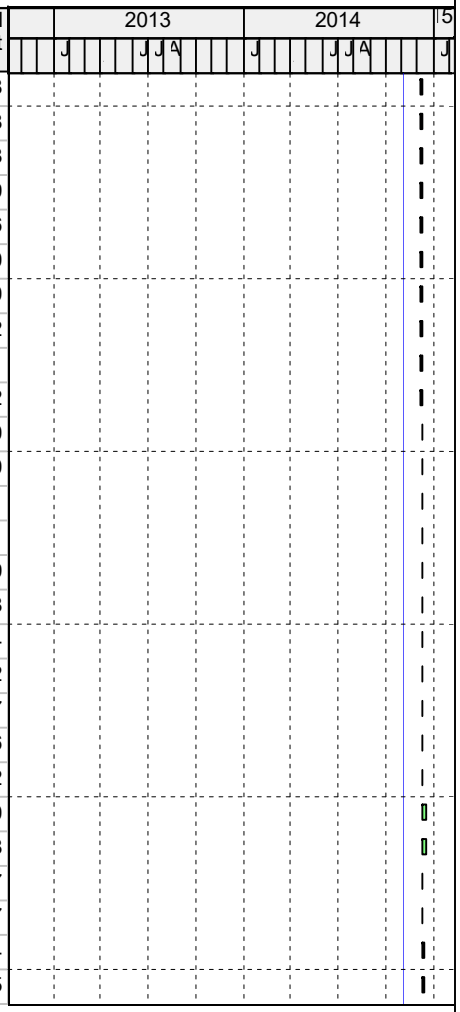



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8618 | L3 Pool - Ceramic tile | 5 | 5 | 10-Dec-14 | 16-Dec-14 | 13 |
| L17-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 10-Dec-14 | 15-Dec-14 | 17 |
| L06-7146 | Final Coat Finish Paint | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 24 |
| I-1610 | Enclosure at manlift - Framing and windows | 4 | 4 | 10-Dec-14 | 15-Dec-14 | 15 |
| L17-8218 | Corridors - Fire Sprinkler Trim | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 5 |
| LL1-Z3-8146 | Install Restroom Accessories | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 26 |
| L16-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 10 |
| L11-8418 | Flooring at Elevator Lobby | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 14 |
| L12-8418 | Flooring at Elevator Lobby | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 14 |
| L14-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 11 |
| L14-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 11-Dec-14 | 11-Dec-14 | 13 |
| L15-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 11 |
| L15-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 11-Dec-14 | 11-Dec-14 | 13 |
| L14-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 11-Dec-14 | 16-Dec-14 | 16 |
| L15-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 11-Dec-14 | 16-Dec-14 | 16 |
| L07-7136 | Install Door and Hardware | 1 | 1 | 11-Dec-14 | 11-Dec-14 | 22 |
| L08-7134 | Install VCT Flooring | 2 | 2 | 11-Dec-14 | 12-Dec-14 | 12 |
| L14-7138 | Electrical Trim-Out | 2 | 2 | 11-Dec-14 | 12-Dec-14 | 16 |
| L14-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 16 |
| L15-7138 | Electrical Trim-Out | 2 | 2 | 11-Dec-14 | 12-Dec-14 | 16 |
| L15-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 16 |
| L14-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 11-Dec-14 | 16-Dec-14 | 16 |
| L15-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 11-Dec-14 | 16-Dec-14 | 16 |
| L1K-8124b | Install Base | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 23 |
| L14-7144 | Fire Sprinkler Trim | 1 | 1 | 11-Dec-14 | 11-Dec-14 | 18 |
| L15-7144 | Fire Sprinkler Trim | 1 | 1 | 11-Dec-14 | 11-Dec-14 | 18 |
| L17-8130 | Install Door Hardware | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 17 |

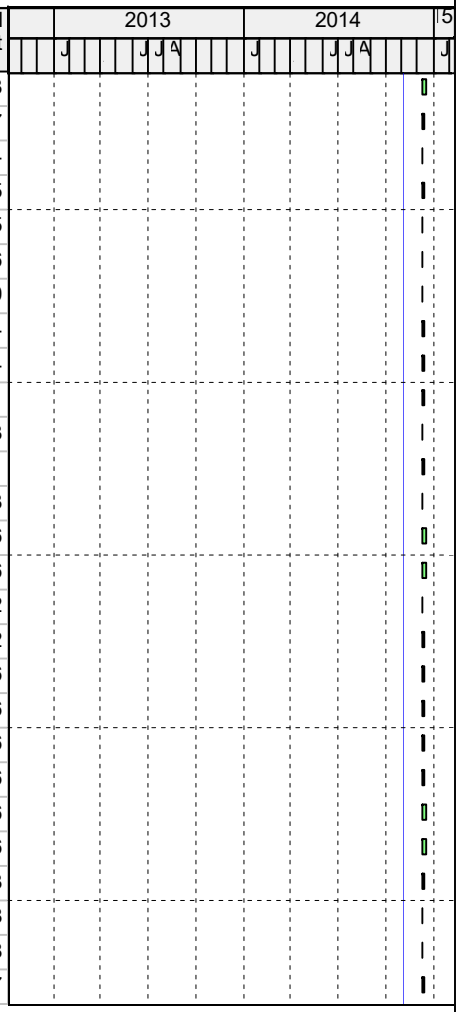



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 17 |
| L10-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 17 |
| L16-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 9 |
| L17-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 8 |
| L07-7146 | Final Coat Finish Paint | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 22 |
| CO-7222 | Cx - Kitchen Equipment Start-Up & Testing | 15 | 15 | 12-Dec-14 | 06-Jan-15 | 20 |
| CO-7224 | Cx - Food Prep Equipment Start-Up & Testing | 15 | 15 | 12-Dec-14 | 06-Jan-15 | 20 |
| CO-7226 | Cx - Laundry Equipment Start-Up & Testing | 15 | 15 | 12-Dec-14 | 06-Jan-15 | 20 |
| CO-7228 | Cx - Pool Equipment Start-Up & Testing | 15 | 15 | 12-Dec-14 | 06-Jan-15 | 20 |
| L17-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 5 |
| L1K-8208 | Install Restroom Accessories | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 23 |
| L1BOH2-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 15-Dec-14 | 16-Dec-14 | 10 |
| L1BOH2-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 15-Dec-14 | 16-Dec-14 | 10 |
| L1BOH2-8204 | Mech Trim / Finish (HVAC & Plumbing) | 2 | 2 | 15-Dec-14 | 16-Dec-14 | 10 |
| L11-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 15-Dec-14 | 16-Dec-14 | 14 |
| L12-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 15-Dec-14 | 16-Dec-14 | 14 |
| L08-7136 | Install Door and Hardware | 1 | 1 | 15-Dec-14 | 15-Dec-14 | 20 |
| L09-7134 | Install VCT Flooring | 2 | 2 | 15-Dec-14 | 16-Dec-14 | 12 |
| I-1604 | Enclosure at manlift - GWB | 6 | 6 | 16-Dec-14 | 23-Dec-14 | 18 |
| I-1608 | Enclosure at manlift - Hat channel & metal panels (El | 8 | 8 | 16-Dec-14 | 29-Dec-14 | 15 |
| L14-8418 | Flooring at Elevator Lobby | 3 | 3 | 16-Dec-14 | 18-Dec-14 | 11 |
| L15-8418 | Flooring at Elevator Lobby | 3 | 3 | 16-Dec-14 | 18-Dec-14 | 11 |
| L16-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 16-Dec-14 | 18-Dec-14 | 9 |
| L16-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 16-Dec-14 | 16-Dec-14 | 11 |
| L17-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 16-Dec-14 | 18-Dec-14 | 8 |
| L17-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 16-Dec-14 | 16-Dec-14 | 10 |
| L16-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 16-Dec-14 | 19-Dec-14 | 14 |

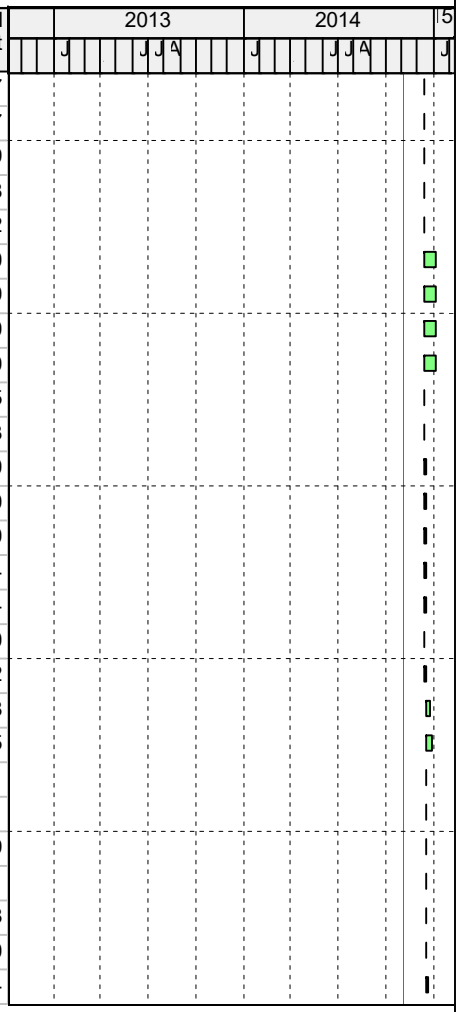



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 16-Dec-14 | 19-Dec-14 | 13 |
| L16-7138 | Electrical Trim-Out | 2 | 2 | 16-Dec-14 | 17-Dec-14 | 15 |
| L16-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 16-Dec-14 | 18-Dec-14 | 15 |
| L17-7138 | Electrical Trim-Out | 2 | 2 | 16-Dec-14 | 17-Dec-14 | 14 |
| L17-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 16-Dec-14 | 18-Dec-14 | 14 |
| L16-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 16-Dec-14 | 19-Dec-14 | 14 |
| L17-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 16-Dec-14 | 19-Dec-14 | 13 |
| L08-7146 | Final Coat Finish Paint | 2 | 2 | 16-Dec-14 | 17-Dec-14 | 20 |
| L16-7144 | Fire Sprinkler Trim | 1 | 1 | 16-Dec-14 | 16-Dec-14 | 17 |
| L17-7144 | Fire Sprinkler Trim | 1 | 1 | 16-Dec-14 | 16-Dec-14 | 17 |
| L17-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 16-Dec-14 | 17-Dec-14 | 15 |
| L1BOH2-8201 | Final Coat Finish Paint | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 18 |
| L11-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 17-Dec-14 | 18-Dec-14 | 14 |
| L12-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 17-Dec-14 | 18-Dec-14 | 14 |
| L03-8620 | L3 Pool - Plumbing Fixtures & Trim / Finish | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 13 |
| L03-8622 | L3 Pool - HVAC trim / Finish | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 13 |
| L03-8624 | L3 Pool - Fire Sprinkler Trim / Finish | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 13 |
| L03-8626 | L3 Pool - Elec Trim/ Finish | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 13 |
| L03-8628 | L3 Pool - Elec Specialties Trim / Finish | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 13 |
| L03-8630 | L3 Pool - Doors & Hardware | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 13 |
| L09-7136 | Install Door and Hardware | 1 | 1 | 17-Dec-14 | 17-Dec-14 | 18 |
| L10-7134 | Install VCT Flooring | 2 | 2 | 17-Dec-14 | 18-Dec-14 | 16 |
| CO-7230 | Cx - TAB: Air Moving Systems, Tower | 10 | 10 | 17-Dec-14 | 02-Jan-15 | 22 |
| CO-7232 | Cx - TAB: Plumbing/HVAC Water Systems, Tower | 10 | 10 | 17-Dec-14 | 02-Jan-15 | 22 |
| CO-7234 | Cx - TAB: Air Moving Systems, Podium | 17 | 17 | 17-Dec-14 | 13-Jan-15 | 15 |
| CO-7236 | Cx - TAB: Plumbing/HVAC Water Systems, Podium | 17 | 17 | 17-Dec-14 | 13-Jan-15 | 15 |
| CO-7238 | Cx - Internal Equipment Verifications (HP) | 17 | 17 | 17-Dec-14 | 13-Jan-15 | 0 |

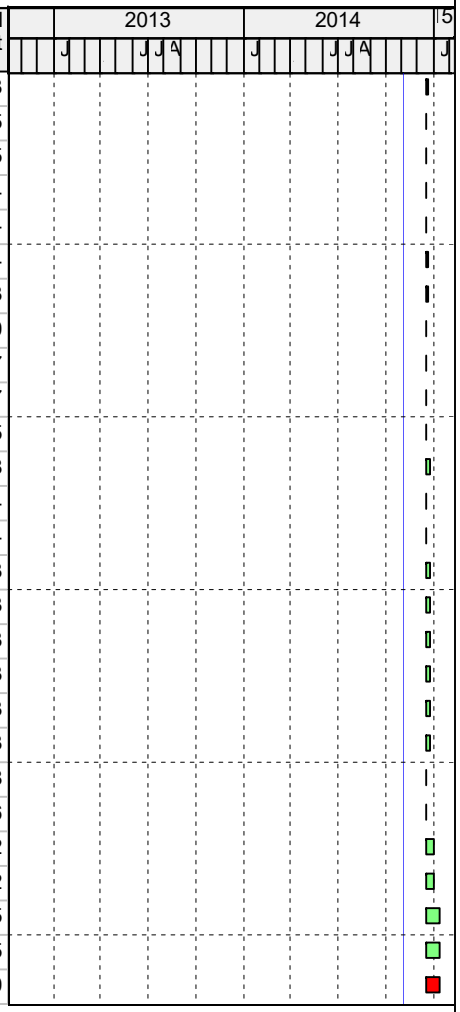


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-3102 | Ballroom ceilings - additional work per ASIs 18, 25 | 4 | 4 | 18-Dec-14 | 23-Dec-14 | 13 |
| L15-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 18-Dec-14 | 19-Dec-14 | 11 |
| L1B-8120 | Install operable partitions | 3 | 3 | 18-Dec-14 | 22-Dec-14 | 14 |
| L03-7134 | Install VCT Flooring & Base | 3 | 3 | 18-Dec-14 | 22-Dec-14 | 13 |
| L1B-8128 | Install Base | 2 | 2 | 18-Dec-14 | 19-Dec-14 | 15 |
| L09-7146 | Final Coat Finish Paint | 2 | 2 | 18-Dec-14 | 19-Dec-14 | 18 |
| L17-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 18-Dec-14 | 19-Dec-14 | 5 |
| L14-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 19-Dec-14 | 22-Dec-14 | 11 |
| L16-8418 | Flooring at Elevator Lobby | 3 | 3 | 19-Dec-14 | 23-Dec-14 | 9 |
| L17-8418 | Flooring at Elevator Lobby | 3 | 3 | 19-Dec-14 | 23-Dec-14 | 8 |
| L10-7136 | Install Door and Hardware | 1 | 1 | 19-Dec-14 | 19-Dec-14 | 16 |
| L11-7134 | Install VCT Flooring | 2 | 2 | 19-Dec-14 | 20-Dec-14 | 16 |
| L12-7134 | Install VCT Flooring | 2 | 2 | 19-Dec-14 | 20-Dec-14 | 16 |
| L14-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 11 |
| L15-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 11 |
| L1K-8128 | Install Kitchen equipment (BY OTHERS) | 5 | 5 | 22-Dec-14 | 30-Dec-14 | 9 |
| L11-7136 | Install Door and Hardware | 1 | 1 | 22-Dec-14 | 22-Dec-14 | 15 |
| L12-7136 | Install Door and Hardware | 1 | 1 | 22-Dec-14 | 22-Dec-14 | 15 |
| L14-7134 | Install VCT Flooring | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 16 |
| L15-7134 | Install VCT Flooring | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 16 |
| L10-7146 | Final Coat Finish Paint | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 16 |
| L16-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 9 |
| L17-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 8 |
| L03-7136 | Install Doors and Hardware | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 13 |
| L11-7146 | Final Coat Finish Paint | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 15 |
| L12-7146 | Final Coat Finish Paint | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 15 |
| L1BOH2-8134 | Clean | 4 | 4 | 24-Dec-14 | 31-Dec-14 | 18 |

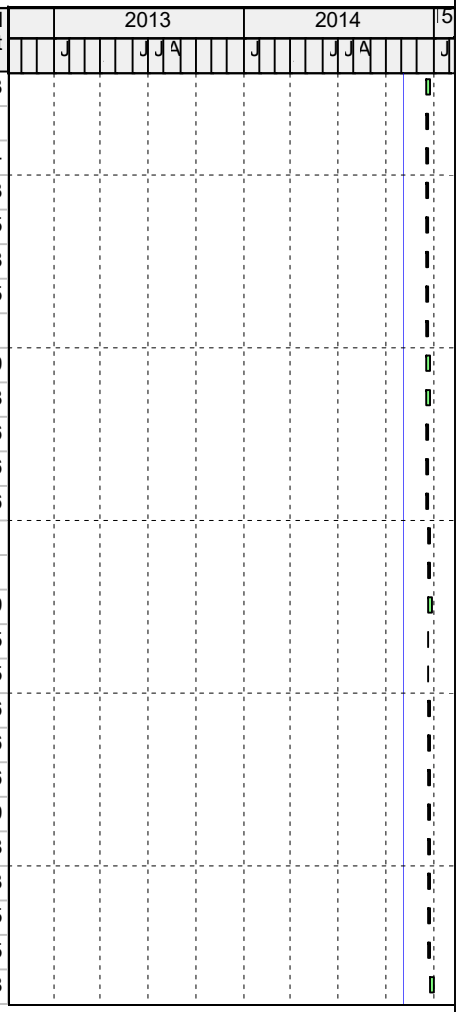



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1BOH2-8132 | Punch | 4 | 4 | 24-Dec-14 | 31-Dec-14 | 18 |
| I-1606 | Enclosure at manlift - Paint & finishes | 4 | 4 | 24-Dec-14 | 31-Dec-14 | 18 |
| L03-8632 | L3 Pool - Install Bathroom Accessories | 3 | 3 | 24-Dec-14 | 30-Dec-14 | 13 |
| L14-7136 | Install Door and Hardware | 1 | 1 | 24-Dec-14 | 24-Dec-14 | 13 |
| L15-7136 | Install Door and Hardware | 1 | 1 | 24-Dec-14 | 24-Dec-14 | 13 |
| L16-7134 | Install VCT Flooring | 2 | 2 | 24-Dec-14 | 26-Dec-14 | 16 |
| L17-7134 | Install VCT Flooring | 2 | 2 | 24-Dec-14 | 26-Dec-14 | 16 |
| L16-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 9 |
| L17-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 8 |
| L16-7136 | Install Door and Hardware | 1 | 1 | 29-Dec-14 | 29-Dec-14 | 13 |
| L17-7136 | Install Door and Hardware | 1 | 1 | 29-Dec-14 | 29-Dec-14 | 13 |
| L03-7146 | Final Coat Finish Paint | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 13 |
| L14-7146 | Final Coat Finish Paint | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 13 |
| L15-7146 | Final Coat Finish Paint | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 13 |
| L16-7146 | Final Coat Finish Paint | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 13 |
| L17-7146 | Final Coat Finish Paint | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 13 |
| I-1612 | Enclosure at manlift - Caulking (Elev 32) | 5 | 5 | 30-Dec-14 | 06-Jan-15 | 15 |
| L1K-8128a | Kitchen Equipment Final Connections | 5 | 5 | 31-Dec-14 | 07-Jan-15 | 9 |
| L1BOH2-81214 | L1, Zone 3 Complete | 0 | 0 | | 31-Dec-14 | 18 |
| CM-1024 | Tower - "Clean/Punch" Complete - All Floors | 0 | 0 | | 07-Jan-15 | 19 |
| L1L-8124a | Install Base | 3 | 3 | 08-Jan-15 | 12-Jan-15 | 2 |
| I-1202 | Concierge Lounge - Additional flooring work | 1 | 1 | 09-Jan-15 | 09-Jan-15 | 1 |
| I-1204 | Concierge Lounge - Additional millwork | 4 | 4 | 09-Jan-15 | 14-Jan-15 | 1 |
| L1L-8120 | Install plumbing at bar | 2 | 2 | 09-Jan-15 | 12-Jan-15 | 2 |
| L1L-8122 | Install electrical at bar | 2 | 2 | 09-Jan-15 | 12-Jan-15 | 2 |
| CO-7112T | City of Bellevue/3rd Party Fire Sprinkler Inspection / A | 5 | 5 | 20-Jan-15 | 26-Jan-15 | 1 |
| CO-7118T | City of Bellevue/3rd Party Fire Alarm Inspection / Appl | 5 | 5 | 20-Jan-15 | 26-Jan-15 | 1 |

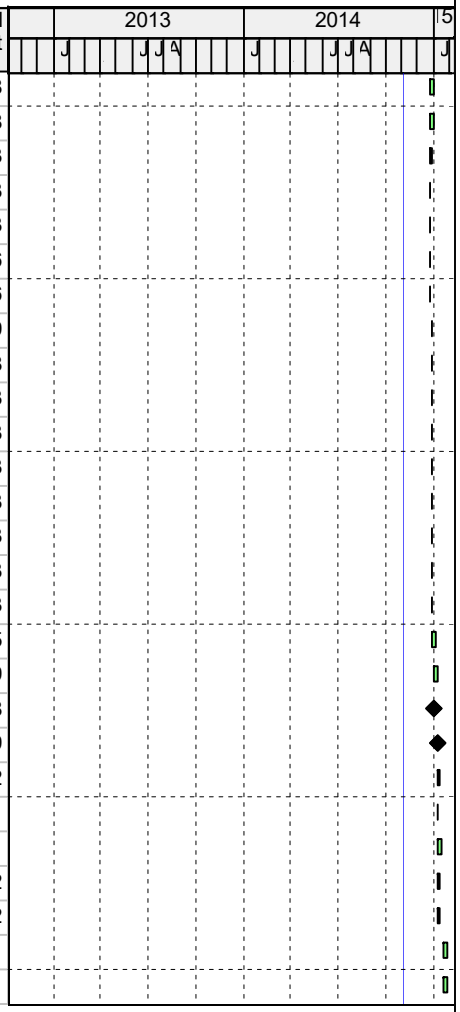



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7106T | City of Bellevue/3rd Party Smoke Control Testing (Tow | 5 | 5 | 20-Jan-15 | 26-Jan-15 | 1 |
| CO-7402 | Cx - Final 3rd Party Commissioning | 10 | 10 | 21-Jan-15 | 03-Feb-15 | 0 |
| CM-1022 | Podium - "Clean/Punch" Complete - All Floors, All Zon | 0 | 0 | | 26-Jan-15 | 6 |
| CO-7124 | Complete Final Building Inspections | 5 | 5 | 27-Jan-15 | 02-Feb-15 | 1 |
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13 A | | |
| CM-1002 | CM - Contract Time (578 Cal Days) | 576 | 0 | 06-Mar-13 A | 05-Oct-14 A | |
| CM-1014 | CM - Start of Construction | 0 | 0 | 05-Apr-13 A | | |
| CM-1006 | Construction Documents Issued by Client - (Due on 7 | 0 | 0 | 03-Nov-14 | | 93 |
| CO-7004 | CO - Prep / Submit O&M Manuals | 40 | 40 | 03-Nov-14 | 12-Dec-14 | 53 |
| CM-1008 | Finalization of Allowances - (Due on 9-2-13) | 0 | 0 | 03-Nov-14 | | 93 |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 17-Nov-14 | | 16 |
| CM-1016 | CM - Owner FF+E "Build-Out" - Floors 4-10 | 14 | 14 | 17-Nov-14 | 30-Nov-14 | 16 |
| CM-1018 | CM - Hotel Operations Training | 21 | 21 | 01-Dec-14 | 21-Dec-14 | 44 |
| CO-7122 | CO - Certificate of Occupancy | 0 | 0 | | 02-Feb-15 | 1 |
| CO-7006 | CO - Certificate of Occupancy/Substantial Completior | 0 | 0 | | 03-Feb-15 | 0 |
| **Misc Milestones** | | | | | | |
| CM-1020 | MM - Site Mobilization | 10 | 0 | 06-Mar-13 A | 04-Apr-13 A | |
| MM-1008 | MM - Top Out - Tower / Structure | 0 | 0 | | 16-Apr-14 A | |
| MM-1004 | MM - Start Drywall In Tower | 0 | 0 | 27-Jun-14 A | | |
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 06-Sep-14 A | |
| MM-1010 | Energize Permanent Power | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| **Tower Crane** | | | | | | |

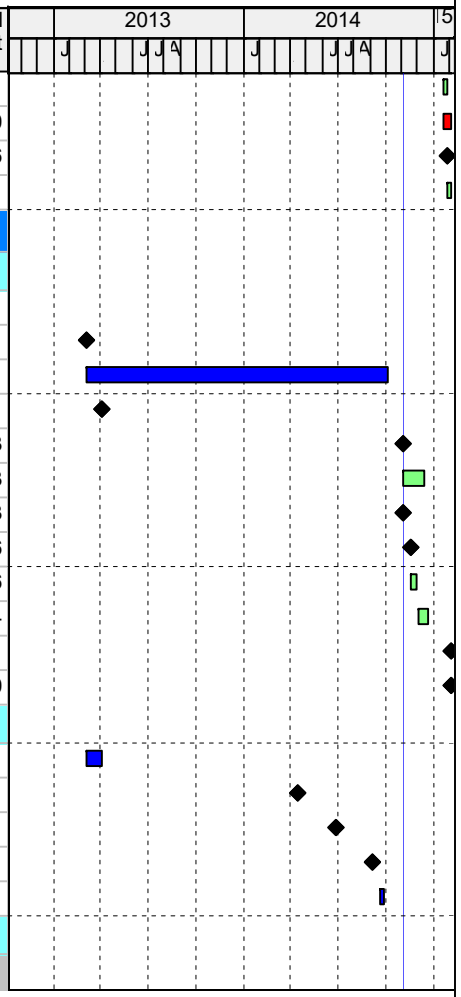



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 0 | 04-Jun-13 A | 14-Jun-13 A | |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 0 | 20-Jun-13 A | 24-Jun-13 A | |
| TC-5902 | Tower Crane - Erectiion | 2 | 0 | 21-Jun-13 A | 24-Jun-13 A | |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 24-Jun-13 A | | |
| TC-5906 | Tower Crane - Operatational Period | 391 | 0 | 24-Jun-13 A | 16-Jun-14 A | |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 0 | 16-Jun-14 A | 17-Jun-14 A | |
| **Man & Material Lifts** | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 0 | 14-Jan-14 A | 20-Jan-14 A | |
| ML-5952 | Man/Material Lifts - Erect/Build Loading Dock | 5 | 0 | 21-Jan-14 A | 27-Jan-14 A | |
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 10-Feb-14 A | | |
| ML-5954 | Man/Material Lifts - Load Test / Certify | 1 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| ML-5958 | Man/Material Lifts - Operatational Period | 196 | 11 | 10-Feb-14 A | 13-Nov-14 | 16 |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 2 | 2 | 14-Nov-14 | 15-Nov-14 | 16 |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |
| **Mass Excavation / Shoring** | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 0 | 05-Apr-13 A | 12-Apr-13 A | |
| SW-2002 | Demolition And Utility Relocation | 8 | 0 | 15-Apr-13 A | 19-Apr-13 A | |
| SW-2010 | Grade Subgrade for Elect/Plumbing | 3 | 0 | 07-Jan-14 A | 09-Jan-14 A | |
| **Site Finishes** | | | | | | |
| SW-2006 | Install Perm Power Electrical Service / Dry Utilities (Ofl | 15 | 0 | 20-May-14 A | 05-Jun-14 A | |
| SW-2004 | Offsite Water & Water Connection | 9 | 0 | 22-Sep-14 A | 01-Oct-14 A | |
| SW-2008 | Zone 4 - Site finishes (summarized) | 20 | 20 | 18-Nov-14 | 24-Dec-14 | 21 |
| **Structure** | | | | | | |
| **Foundation / Substructure - (Levels LL4 / LL3)** | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |

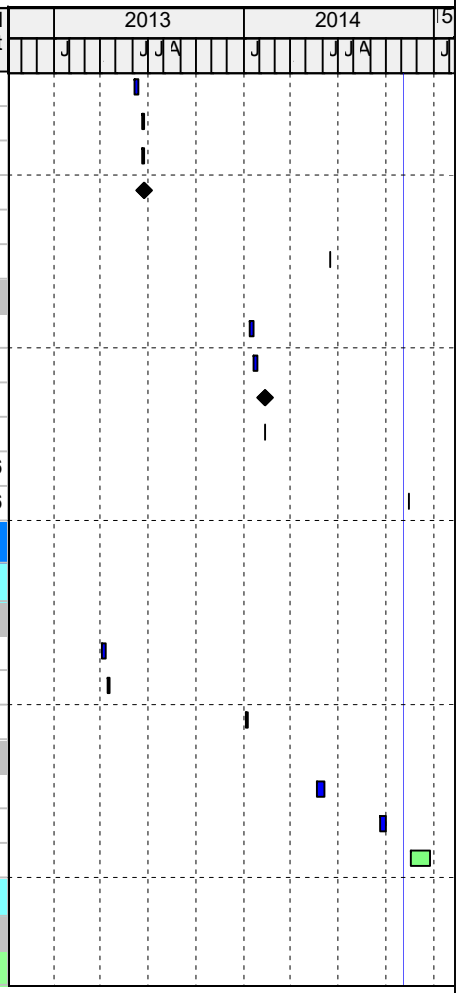



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 0 | 12-Jun-13 A | 27-Jun-13 A | |
| LL4-1601 | LL4 - Excavate Footings | 14 | 0 | 17-Jun-13 A | 30-Jul-13 A | |
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 0 | 18-Jun-13 A | 24-Jun-13 A | |
| LL4-1606 | LL4 - Undrgmd Plumbing | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-1608 | LL4 - Undrgmd Elec | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 0 | 19-Jun-13 A | 25-Jun-13 A | |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 0 | 26-Jun-13 A | 02-Aug-13 A | |
| LL4-2033 | LL4 - Shotcrete Walls | 27 | 0 | 26-Jun-13 A | 05-Aug-13 A | |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 0 | 03-Jul-13 A | 21-Aug-13 A | |
| LL4-1614 | LL4 - FRP SOG | 5 | 0 | 10-Jul-13 A | 07-Aug-13 A | |
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 0 | 12-Jul-13 A | 26-Jul-13 A | |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 0 | 13-Jul-13 A | 06-Aug-13 A | |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 0 | 22-Jul-13 A | 24-Jul-13 A | |
| LL4-1618 | LL4 - FRP Ramp SOG | 5 | 0 | 01-Aug-13 A | 07-Aug-13 A | |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2004 | LL2 - Shore / Form Deck | 8 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2006 | LL3 - M & E Inserts | 4 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2008 | LL3 - ReSteel / PT Cables | 6 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2010 | LL3 - Install Embeds | 2 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2001 | LL3 - Waterproof Walls | 3 | 0 | 05-Aug-13 A | 05-Aug-13 A | |
| LL3-2012 | LL3 - Pour / Finish Deck | 2 | 0 | 16-Aug-13 A | 16-Aug-13 A | |
| LL3-2014 | LL3 - Stress Tendons | 1 | 0 | 19-Aug-13 A | 19-Aug-13 A | |
| LL3-2000 | LL3 - FRP Core Walls | 8 | 0 | 19-Aug-13 A | 28-Aug-13 A | |
| LL3-2033 | LL3 - Shotcrete Walls | 5 | 0 | 23-Aug-13 A | 26-Aug-13 A | |
| LL3-2016 | LL3 - Strip / ReShore Deck | 3 | 0 | 01-Sep-13 A | 13-Sep-13 A | |
| LL3-2018 | LL3 - Remove ReShores | 4 | 0 | 04-Nov-13 A | 07-Nov-13 A | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |

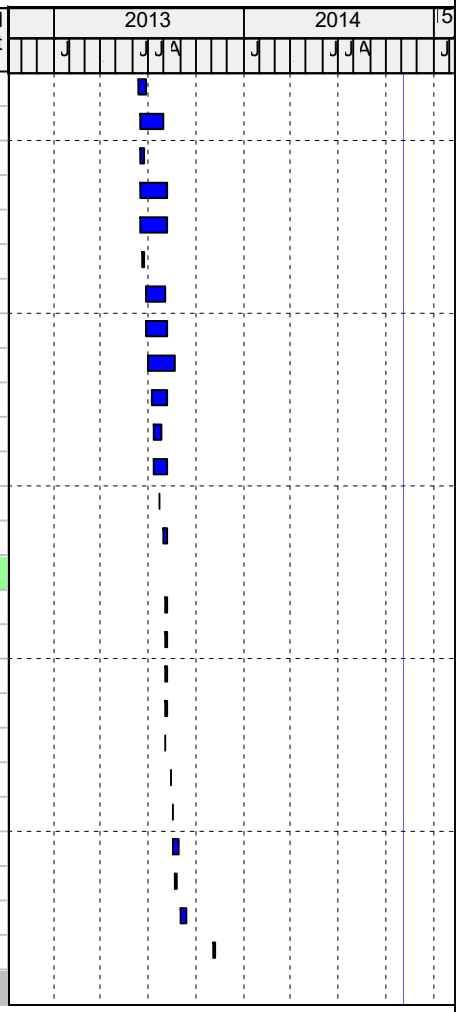



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Grids 1 to 4 - (SOG @ Loading Dock)** | | | | | | |
| LL2-2056 | LL2 - Grease Intercepter | 5 | 0 | 15-Aug-13 A | 21-Aug-13 A | |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 0 | 27-Aug-13 A | 04-Sep-13 A | |
| LL2-2027 | LL2 - Waterproof Walls | 2 | 0 | 27-Aug-13 A | 28-Aug-13 A | |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 0 | 30-Aug-13 A | 05-Sep-13 A | |
| LL2-2021 | LL2 - FRP Elec Vault | 14 | 0 | 30-Aug-13 A | 04-Sep-13 A | |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 0 | 04-Sep-13 A | 11-Sep-13 A | |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 0 | 11-Sep-13 A | 13-Sep-13 A | |
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls/Roof | 11 | 0 | 19-Sep-13 A | 03-Oct-13 A | |
| LL2-2020 | LL2 - Undrgmd Plumbing | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2022 | LL2 - Undrgmd Elec | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2031 | LL2 - FRP Generator SOG | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2015 | LL2 to LL1 FRP Columns / Misc Walls | 6 | 0 | 01-Oct-13 A | 01-Oct-13 A | |
| LL2-2029 | LL2 - F/R/P Pour #2 | 8 | 0 | 15-Jan-14 A | 24-Jan-14 A | |
| LL2-2011 | LL2 - F/R/P Pour #3 | 16 | 0 | 24-Jan-14 A | 18-Feb-14 A | |
| LL2-2019 | LL2 - F/R/P Pour #6 | 4 | 0 | 19-Feb-14 A | 17-Mar-14 A | |
| LL2-2044 | LL2 - Set Generator | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |
| LL2-2004 | LL2 - Shore / Form Deck | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2035 | LL2 to LL1 - Shotcrete Walls | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2006 | LL2 - M & E Inserts | 4 | 0 | 14-Aug-13 A | 19-Aug-13 A | |
| LL2-2008 | LL2 - ReSteel / PT Cables | 6 | 0 | 14-Aug-13 A | 21-Aug-13 A | |
| LL2-2010 | LL2 - Install Embeds | 3 | 0 | 14-Aug-13 A | 16-Aug-13 A | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 0 | 27-Aug-13 A | 06-Sep-13 A | |
| LL2-2012 | LL2 - Place / Finish Deck | 3 | 0 | 29-Aug-13 A | 29-Aug-13 A | |

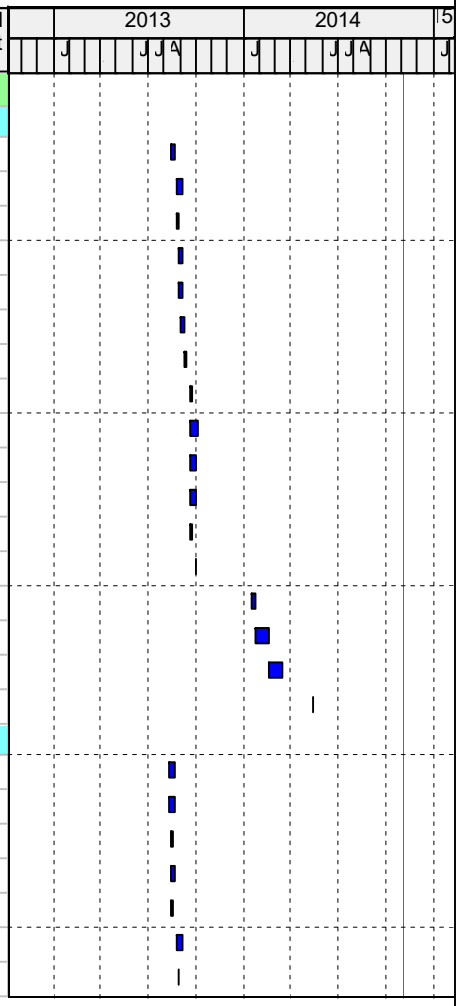


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2023 | LL2 - Waterproof Walls | 3 | 0 | 29-Aug-13 A | 03-Sep-13 A | |
| LL2-2014 | LL2 - Stress Tendons | 1 | 0 | 30-Aug-13 A | 30-Aug-13 A | |
| LL2-2016 | LL2 - Strip / ReShore | 3 | 0 | 03-Sep-13 A | 05-Sep-13 A | |
| LL2-8234 | LL2 - Place / Finish Deck | 3 | 0 | 12-Sep-13 A | 12-Sep-13 A | |
| LL2-2000 | LL2 - FRP Core Walls | 8 | 0 | 12-Sep-13 A | 23-Sep-13 A | |
| LL2-2018 | LL2 - Remove ReShores | 4 | 0 | 13-Nov-13 A | 18-Nov-13 A | |
| LL2-2013 | LL2 - F/R/P Pour #1 | 4 | 0 | 13-Jan-14 A | 16-Jan-14 A | |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| P5A-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2000 | LL1 - FRP Core Walls | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2004 | LL1 - Shore / Form Deck | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| P6-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P6-2004 | LL1 - Shore / Form Deck | 7 | 0 | 16-Sep-13 A | 24-Sep-13 A | |
| P5A-2006 | LL1 - MEP Rough In | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2008 | LL1 - ReSteel / PT Cables | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2012 | LL1 - Place / Finish Deck | 0 | 0 | 20-Sep-13 A | | |
| P5A-2020 | LL1 - Waterproof Walls | 3 | 0 | 20-Sep-13 A | 24-Sep-13 A | |
| P5A-2014 | LL1 - Stress Tendons | 1 | 0 | 23-Sep-13 A | 23-Sep-13 A | |
| P5A-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2006 | LL1 - MEP Rough In | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2008 | LL1 - ReSteel / PT Cables | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 24-Sep-13 A | 25-Sep-13 A | |
| P6-2020 | LL1 - Waterproof Walls | 4 | 0 | 24-Sep-13 A | 27-Sep-13 A | |
| P5A-2033 | LL1 - Resteel/Shotcrete Walls | 3 | 0 | 25-Sep-13 A | 27-Sep-13 A | |
| P5B-2002 | LL1 - FRP Columns Below | 5 | 0 | 26-Sep-13 A | 02-Oct-13 A | |
| P5B-2004 | LL1 - Shore / Form Deck | 7 | 0 | 26-Sep-13 A | 04-Oct-13 A | |

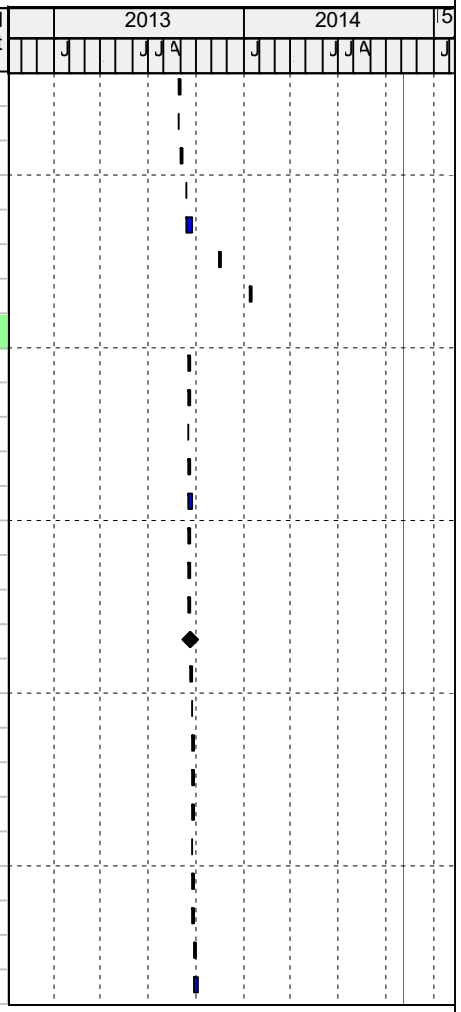



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P6-2012 | LL1 - Place / Finish Deck | 0 | 0 | 27-Sep-13 A | | |
| P6-2014 | LL1 - Stress Tendons | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2033 | LL1 - Resteel/Shotcrete Walls | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 01-Oct-13 A | 03-Oct-13 A | |
| P5B-2006 | LL1 - MEP Rough In | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2002 | FRP Columns Below | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2004 | Shore / Form Deck | 4 | 0 | 03-Oct-13 A | 08-Oct-13 A | |
| P5B-2008 | LL1 - ReSteel / PT Cables | 5 | 0 | 04-Oct-13 A | 10-Oct-13 A | |
| P5B-2010 | LL1 - Install Edgeform/Embeds | 4 | 0 | 04-Oct-13 A | 09-Oct-13 A | |
| P8-2002 | FRP Columns Below | 5 | 0 | 07-Oct-13 A | 11-Oct-13 A | |
| P8-2000 | Form/Resteel/Close Core Walls | 14 | 0 | 07-Oct-13 A | 24-Oct-13 A | |
| P8-2004 | Shore / Form Deck P8 | 8 | 0 | 07-Oct-13 A | 16-Oct-13 A | |
| P7-2002 | FRP Columns Below | 5 | 0 | 08-Oct-13 A | 14-Oct-13 A | |
| P7-2004 | Shore / Form Deck | 6 | 0 | 08-Oct-13 A | 15-Oct-13 A | |
| P10A--2006 | MEP Rough In | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2008 | ReSteel / PT Cables | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2010 | Install Edgeform/Embeds | 2 | 0 | 08-Oct-13 A | 09-Oct-13 A | |
| P5B-2012 | LL1 - Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P10A--2012 | Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P5B-2014 | LL1 - Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P7-2006 | MEP Rough In | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P7-2008 | ReSteel / PT Cables | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P10A--2014 | Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P8-2020 | Shore / Form Deck P9 | 6 | 0 | 14-Oct-13 A | 21-Oct-13 A | |
| P5B-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2010 | Install Edgeform/Embeds | 2 | 0 | 15-Oct-13 A | 16-Oct-13 A | |
| P8-2006 | MEP Rough In | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |

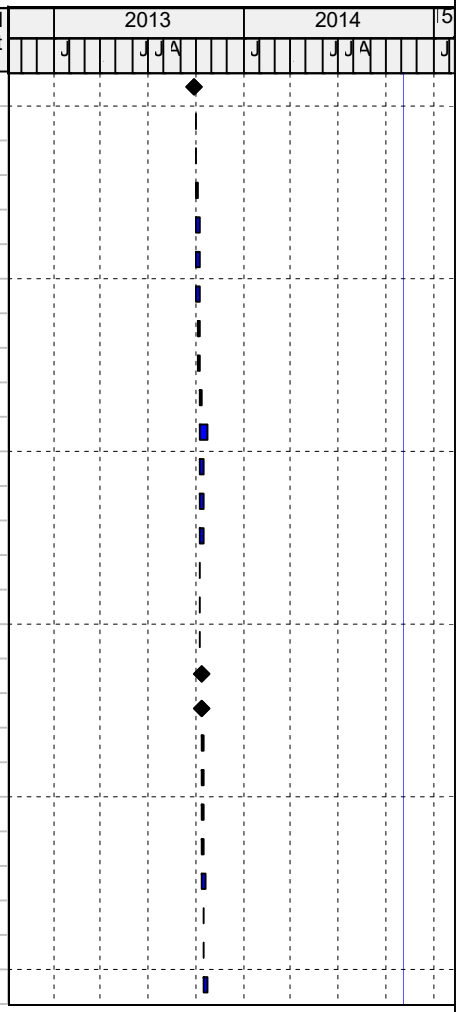


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P8-2008 | ReSteel / PT Cables | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2010 | Install Edgeform/Embeds | 4 | 0 | 15-Oct-13 A | 18-Oct-13 A | |
| P10A--2016 | Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2012 | Place / Finish Deck | 0 | 0 | 18-Oct-13 A | | |
| P7-2033 | Resteel/Shotcrete Walls | 3 | 0 | 18-Oct-13 A | 22-Oct-13 A | |
| P7-2014 | Stress Tendons | 1 | 0 | 21-Oct-13 A | 21-Oct-13 A | |
| P7-2016 | Strip / ReShore Deck | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2002 | FRP Columns Below | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P10B--2000 | FRP Shear Walls Below | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2004 | Shore / Form Deck | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P8-2012 | Place / Finish Deck P 8 & 9 and Core Walls | 0 | 0 | 25-Oct-13 A | | |
| P8-2014 | Stress Tendons | 1 | 0 | 28-Oct-13 A | 28-Oct-13 A | |
| P10B--2006 | MEP Rough In | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2008 | ReSteel / PT Cables | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2010 | Install Edgeform/Embeds | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P12--2002 | FRP Columns Below | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P12--2000 | Form/Resteel/Close Core Walls | 9 | 0 | 28-Oct-13 A | 07-Nov-13 A | |
| P12--2004 | Shore / Form Deck | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P8-2016 | Strip / ReShore Deck | 3 | 0 | 29-Oct-13 A | 31-Oct-13 A | |
| P11--2002 | FRP Columns Below | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P11--2004 | Shore / Form Deck | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P10B--2012 | Place / Finish Deck | 0 | 0 | 31-Oct-13 A | | |
| P10B--2014 | Stress Tendons | 1 | 0 | 01-Nov-13 A | 01-Nov-13 A | |
| P12--2006 | MEP Rough In | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12--2008 | ReSteel / PT Cables | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12--2010 | Install Edgeform/Embeds | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P10B--2016 | Strip / ReShore Deck | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |

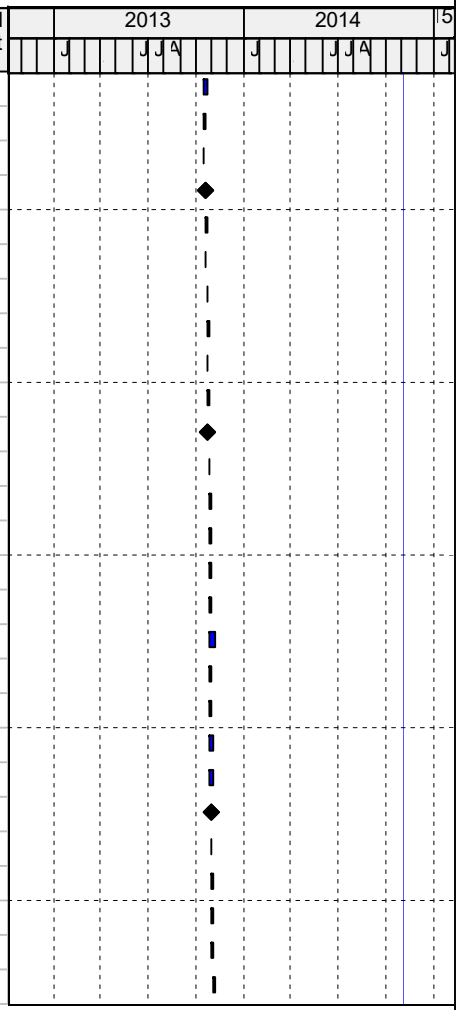



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P11–2006 | MEP Rough In | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2008 | ReSteel / PT Cables | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2010 | Install Edgeform/Embeds | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2012 | Place / Finish Deck | 0 | 0 | 07-Nov-13 A | | |
| P13–2002 | FRP Columns Below | 5 | 0 | 07-Nov-13 A | 14-Nov-13 A | |
| P13–2004 | Shore / Form Deck | 9 | 0 | 07-Nov-13 A | 28-Nov-13 A | |
| P11–2014 | Stress Tendons | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| P12–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 08-Nov-13 A | | |
| P11–2016 | Strip / ReShore Deck | 3 | 0 | 12-Nov-13 A | 14-Nov-13 A | |
| P12–2014 | Stress Tendons | 1 | 0 | 12-Nov-13 A | 12-Nov-13 A | |
| P14–2002 | FRP Columns Below | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P14–2000 | Form/Resteel/Close Core Walls | 8 | 0 | 19-Nov-13 A | 03-Dec-13 A | |
| P14–2004 | Shore / Form Deck | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P13A–2002 | FRP Columns Below | 5 | 0 | 21-Nov-13 A | 27-Nov-13 A | |
| P13A–2004 | Shore / Form Deck | 4 | 0 | 21-Nov-13 A | 26-Nov-13 A | |
| P13–2010 | Install Edgeform/Embeds | 5 | 0 | 22-Nov-13 A | 04-Dec-13 A | |
| P13–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2006 | MEP Rough In | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2010 | Install Edgeform/Embeds | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P13–2006 | MEP Rough In | 5 | 0 | 26-Nov-13 A | 03-Dec-13 A | |
| P13A–2006 | MEP Rough In | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2008 | ReSteel / PT Cables | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2010 | Install Edgeform/Embeds | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13–2012 | Place / Finish Deck | 0 | 0 | 02-Dec-13 A | | |
| P13A–2012 | Place / Finish Deck | 0 | 0 | 03-Dec-13 A | | |
| P14–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 04-Dec-13 A | | |

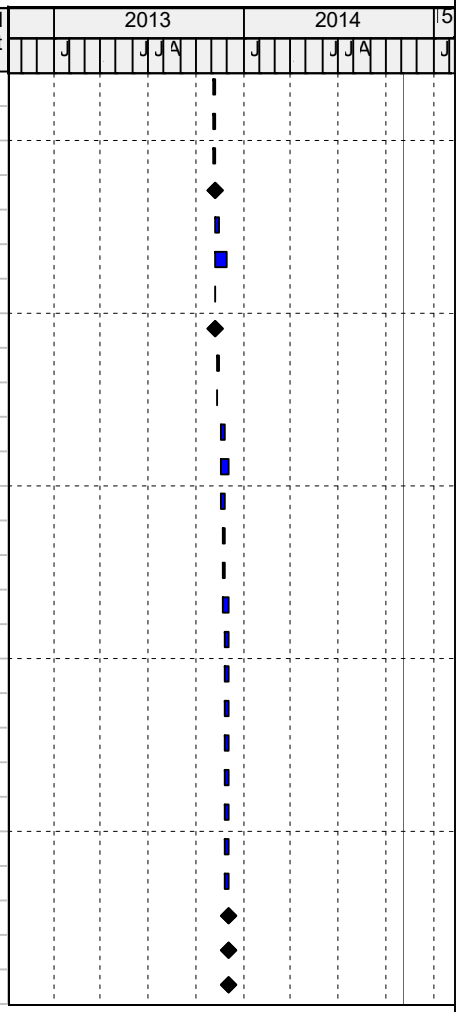


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P13–2014 | Stress Tendons | 1 | 0 | 05-Dec-13 A | 05-Dec-13 A | |
| P15–2002 | FRP Columns Below | 3 | 0 | 05-Dec-13 A | 09-Dec-13 A | |
| P15–2000 | Jump/Resteel/Close Core | 9 | 0 | 05-Dec-13 A | 17-Dec-13 A | |
| P15–2004 | Shore / Form Deck | 5 | 0 | 05-Dec-13 A | 11-Dec-13 A | |
| P13–2016 | Strip / ReShore Deck | 3 | 0 | 06-Dec-13 A | 10-Dec-13 A | |
| P13A–2014 | Stress Tendons | 1 | 0 | 06-Dec-13 A | 06-Dec-13 A | |
| P14–2014 | Stress Tendons | 1 | 0 | 07-Dec-13 A | 07-Dec-13 A | |
| P15–2006 | MEP Rough In | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2008 | ReSteel / PT Cables | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2010 | Install Edgeform/Embeds | 3 | 0 | 11-Dec-13 A | 13-Dec-13 A | |
| P16-2002 | FRP Columns Below | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P16-2004 | Shore / Form Deck | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P15–2012 | Place / Finish Deck | 0 | 0 | 18-Dec-13 A | | |
| P15–2020 | Place Conc @ Core | 0 | 0 | 18-Dec-13 A | | |
| P16-2000 | Jump/Resteel/Close Core | 5 | 0 | 18-Dec-13 A | 24-Dec-13 A | |
| P16-2006 | MEP Rough In | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2008 | ReSteel / PT Cables | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2010 | Install Edgeform/Embeds | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P15–2014 | Stress Tendons | 1 | 0 | 21-Dec-13 A | 21-Dec-13 A | |
| P8-2018 | Remove Reshores | 2 | 0 | 23-Dec-13 A | 24-Dec-13 A | |
| P10A–2018 | Remove Reshores | 2 | 0 | 26-Dec-13 A | 27-Dec-13 A | |
| P16-2012 | Place / Finish Deck | 0 | 0 | 26-Dec-13 A | | |
| P16-2020 | Place Conc @ Core | 0 | 0 | 26-Dec-13 A | | |
| P17-2002 | FRP Columns Below | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P17-2000 | Jump/Resteel/Close Core | 7 | 0 | 27-Dec-13 A | 07-Jan-14 A | |
| P17-2004 | Shore / Form Deck | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P10B–2018 | Remove Reshores | 2 | 0 | 30-Dec-13 A | 31-Dec-13 A | |

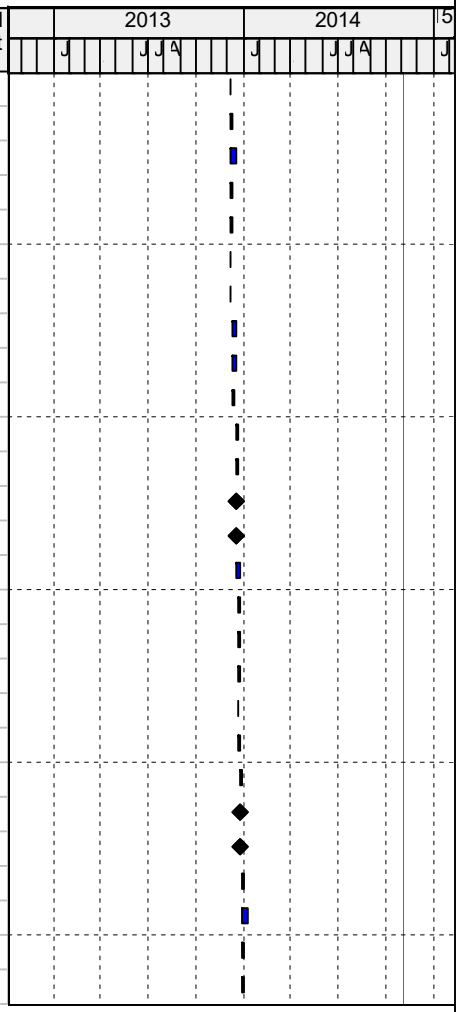



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P16-2014 | Stress Tendons | 1 | 0 | 31-Dec-13 A | 31-Dec-13 A | |
| P5A-2018 | LL1 - Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P11–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P12–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P17-2006 | MEP Rough In | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2008 | ReSteel / PT Cables | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2010 | Install Edgeform/Embeds | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P6-2018 | LL1 - Remove Reshores | 2 | 0 | 06-Jan-14 A | 07-Jan-14 A | |
| P5B-2018 | LL1 - Remove Reshores | 2 | 0 | 08-Jan-14 A | 09-Jan-14 A | |
| P17-2012 | Place / Finish Deck | 0 | 0 | 08-Jan-14 A | | |
| P17-2020 | Place Conc @ Core | 0 | 0 | 08-Jan-14 A | | |
| P18-2002 | FRP Columns Below | 5 | 0 | 09-Jan-14 A | 15-Jan-14 A | |
| P18-2000 | Jump/Resteel/Close Core | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P18-2004 | Shore / Form Deck | 3 | 0 | 09-Jan-14 A | 13-Jan-14 A | |
| LL2-2022R | MEP Rough In | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P7-2018 | Remove Reshores | 2 | 0 | 10-Jan-14 A | 13-Jan-14 A | |
| P17-2014 | Stress Tendons | 1 | 0 | 11-Jan-14 A | 11-Jan-14 A | |
| P13–2018 | Remove Reshores | 2 | 0 | 13-Jan-14 A | 14-Jan-14 A | |
| P13A–2018 | Remove Reshores | 2 | 0 | 15-Jan-14 A | 16-Jan-14 A | |
| WEA-2012 | WIND IMPACT | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| P18-2006 | MEP Rough In | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2008 | ReSteel / PT Cables | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2010 | Install Edgeform/Embeds | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2012 | Place / Finish Deck | 0 | 0 | 22-Jan-14 A | | |
| P18-2020 | Place Conc @ Core | 0 | 0 | 22-Jan-14 A | | |
| P19-2002 | FRP Columns Below | 5 | 0 | 23-Jan-14 A | 29-Jan-14 A | |
| P19-2000 | Jump/Resteel/Close Core | 4 | 0 | 23-Jan-14 A | 28-Jan-14 A | |

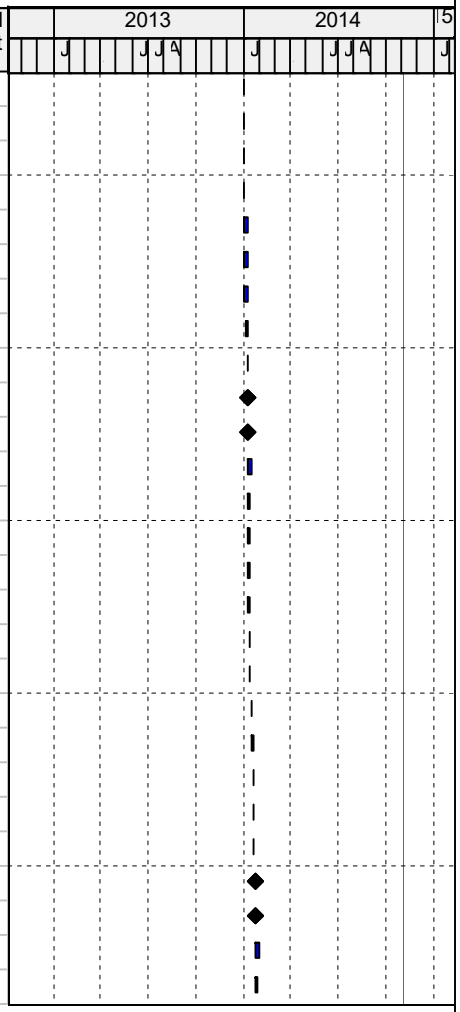


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P19-2004 | Shore / Form Deck | 3 | 0 | 23-Jan-14 A | 27-Jan-14 A | |
| P18-2014 | Stress Tendons | 1 | 0 | 25-Jan-14 A | 25-Jan-14 A | |
| P14–2018 | Remove Reshores | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2006 | MEP Rough In | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2008 | ReSteel / PT Cables | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2010 | Install Edgeform/Embeds | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2012 | Place / Finish Deck | 0 | 0 | 29-Jan-14 A | | |
| P19-2020 | Place Conc @ Core | 0 | 0 | 29-Jan-14 A | | |
| P20-2002 | FRP Columns Below | 5 | 0 | 30-Jan-14 A | 05-Feb-14 A | |
| P20-2000 | Jump/Resteel/Close Core | 9 | 0 | 30-Jan-14 A | 11-Feb-14 A | |
| P20-2004 | Shore / Form Deck | 6 | 0 | 30-Jan-14 A | 10-Feb-14 A | |
| P19-2014 | Stress Tendons | 1 | 0 | 01-Feb-14 A | 01-Feb-14 A | |
| P13A–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P14–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P15–2016 | Strip / ReShore Deck | 3 | 0 | 06-Feb-14 A | 10-Feb-14 A | |
| P20-2006 | MEP Rough In | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2008 | ReSteel / PT Cables | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2010 | Install Edgeform/Embeds | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| L03-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 06-Feb-14 A | 12-Feb-14 A | |
| P16-2016 | Strip / ReShore Deck | 3 | 0 | 10-Feb-14 A | 12-Feb-14 A | |
| L04-2018 | Remove Reshores | 2 | 0 | 10-Feb-14 A | 11-Feb-14 A | |
| L03-2018 | Remove Reshores | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| P17-2016 | Strip / ReShore Deck | 3 | 0 | 12-Feb-14 A | 14-Feb-14 A | |
| P20-2012 | Place / Finish Deck | 0 | 0 | 12-Feb-14 A | | |
| P20-2020 | Place Conc @ Core | 0 | 0 | 12-Feb-14 A | | |
| L04-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-Feb-14 A | 18-Feb-14 A | |
| P12–2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |

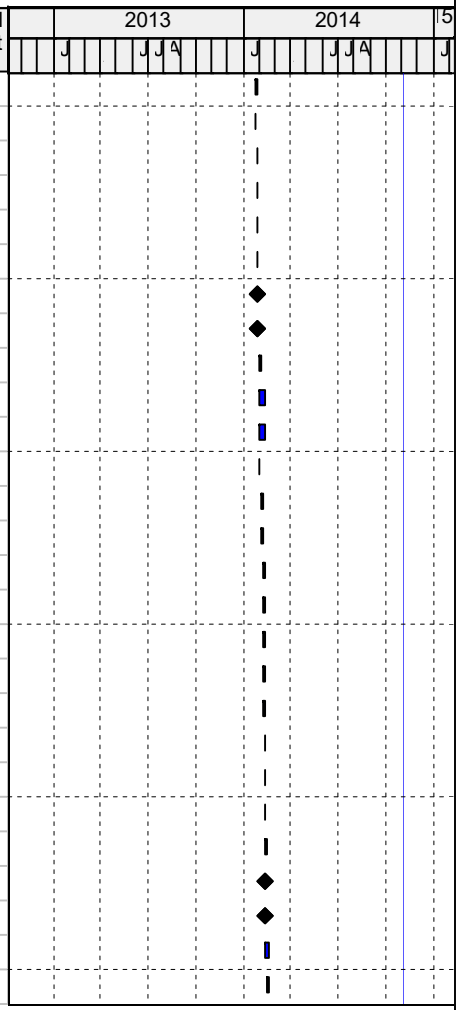


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P18-2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P21-2002 | FRP Columns Below | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| P21-2000 | Jump/Resteel/Close Core | 4 | 0 | 13-Feb-14 A | 18-Feb-14 A | |
| P21-2004 | Shore / Form Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P19-2016 | Strip / ReShore Deck | 3 | 0 | 14-Feb-14 A | 18-Feb-14 A | |
| P20-2014 | Stress Tendons | 1 | 0 | 15-Feb-14 A | 15-Feb-14 A | |
| P21-2006 | MEP Rough In | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2008 | ReSteel / PT Cables | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P20-2016 | Strip / ReShore Deck | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| L05-2018 | Remove Reshores | 2 | 0 | 18-Feb-14 A | 19-Feb-14 A | |
| P21-2012 | Place / Finish Deck | 0 | 0 | 19-Feb-14 A | | |
| P21-2020 | Place Conc @ Core | 0 | 0 | 19-Feb-14 A | | |
| P22-2002 | FRP Columns Below | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P22-2000 | Jump/Resteel/Close Core | 4 | 0 | 20-Feb-14 A | 25-Feb-14 A | |
| P22-2004 | Shore / Form Deck | 3 | 0 | 20-Feb-14 A | 24-Feb-14 A | |
| L05-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P21-2014 | Stress Tendons | 1 | 0 | 22-Feb-14 A | 22-Feb-14 A | |
| P21-2016 | Strip / ReShore Deck | 3 | 0 | 24-Feb-14 A | 26-Feb-14 A | |
| P22-2006 | MEP Rough In | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2008 | ReSteel / PT Cables | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| L06-2018 | Remove Reshores | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| P22-2012 | Place / Finish Deck | 0 | 0 | 26-Feb-14 A | | |
| P22-2020 | Place Conc @ Core | 0 | 0 | 26-Feb-14 A | | |
| P23-2002 | FRP Columns Below | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2000 | Jump/Resteel/Close Core | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |

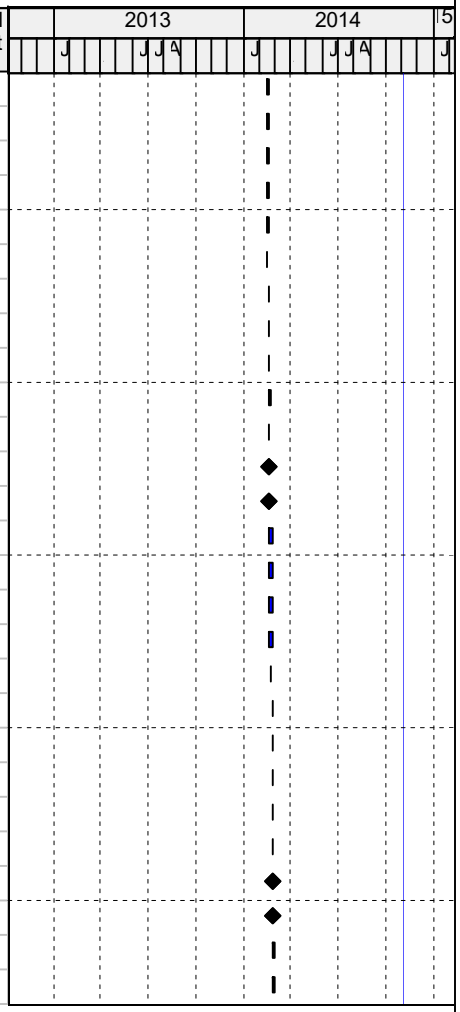



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P23-2004 | Shore / Form Deck | 3 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2006 | MEP Rough In | 2 | 0 | 01-Mar-14 A | 03-Mar-14 A | |
| P22-2014 | Stress Tendons | 1 | 0 | 01-Mar-14 A | 01-Mar-14 A | |
| P23-2008 | ReSteel / PT Cables | 2 | 0 | 03-Mar-14 A | 04-Mar-14 A | |
| P22-2016 | Strip / ReShore Deck | 3 | 0 | 04-Mar-14 A | 10-Mar-14 A | |
| P23-2010 | Install Edgeform/Embeds | 2 | 0 | 04-Mar-14 A | 04-Mar-14 A | |
| L07-2018 | Remove Reshores | 2 | 0 | 04-Mar-14 A | 05-Mar-14 A | |
| P23-2012 | Place / Finish Deck | 0 | 0 | 05-Mar-14 A | | |
| P23-2020 | Place Conc @ Core | 0 | 0 | 05-Mar-14 A | | |
| P24-2002 | FRP Columns Below | 5 | 0 | 05-Mar-14 A | 07-Mar-14 A | |
| P24-2004 | Shore / Form Deck | 3 | 0 | 06-Mar-14 A | 10-Mar-14 A | |
| P24-2000 | Jump/Resteel/Close Core | 4 | 0 | 08-Mar-14 A | 10-Mar-14 A | |
| P23-2014 | Stress Tendons | 1 | 0 | 10-Mar-14 A | 10-Mar-14 A | |
| P24-2008 | ReSteel / PT Cables | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P24-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P23-2016 | Strip / ReShore Deck | 3 | 0 | 11-Mar-14 A | 17-Mar-14 A | |
| P24-2006 | MEP Rough In | 2 | 0 | 11-Mar-14 A | 11-Mar-14 A | |
| P25-2002 | FRP Columns Below | 5 | 0 | 11-Mar-14 A | 13-Mar-14 A | |
| L08-2018 | Remove Reshores | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| P24-2012 | Place / Finish Deck | 0 | 0 | 12-Mar-14 A | | |
| P24-2020 | Place Conc @ Core | 0 | 0 | 12-Mar-14 A | | |
| P25-2004 | Shore / Form Deck | 3 | 0 | 13-Mar-14 A | 17-Mar-14 A | |
| P25-2000 | Jump/Resteel/Close Core | 4 | 0 | 15-Mar-14 A | 17-Mar-14 A | |
| P24-2014 | Stress Tendons | 1 | 0 | 17-Mar-14 A | 17-Mar-14 A | |
| P25-2006 | MEP Rough In | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2008 | ReSteel / PT Cables | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |

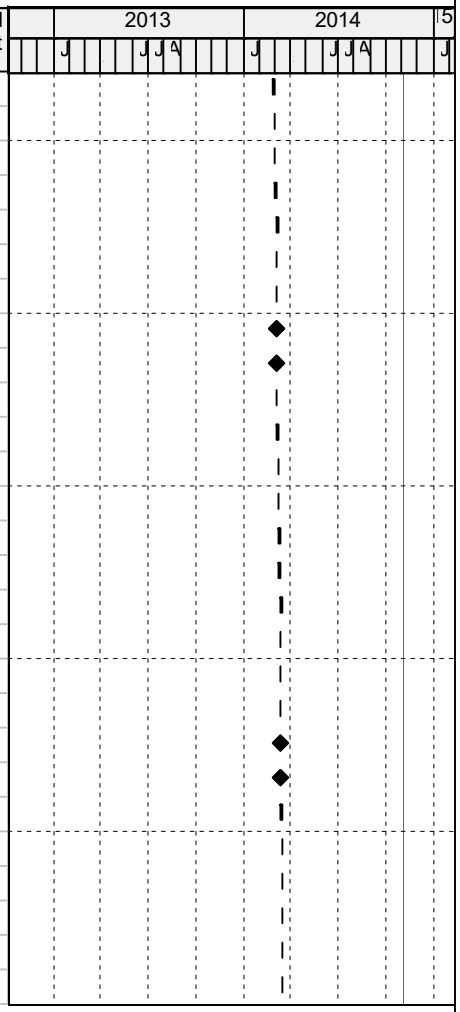


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 18-Mar-14 A | 20-Mar-14 A | |
| L09-2018 | Remove Reshores | 2 | 0 | 18-Mar-14 A | 19-Mar-14 A | |
| P26-2002 | FRP Columns Below | 5 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| P25-2012 | Place / Finish Deck | 0 | 0 | 19-Mar-14 A | | |
| P25-2020 | Place Conc @ Core | 0 | 0 | 19-Mar-14 A | | |
| P26-2004 | Shore / Form Deck | 3 | 0 | 20-Mar-14 A | 24-Mar-14 A | |
| L07-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 21-Mar-14 A | 25-Mar-14 A | |
| P26-2000 | Jump/Resteel/Close Core | 4 | 0 | 22-Mar-14 A | 24-Mar-14 A | |
| P26-2006 | MEP Rough In | 2 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P26-2008 | ReSteel / PT Cables | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P26-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P25-2014 | Stress Tendons | 1 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P27-2002 | FRP Columns Below | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| P26-2012 | Place / Finish Deck | 0 | 0 | 26-Mar-14 A | | |
| P26-2020 | Place Conc @ Core | 0 | 0 | 26-Mar-14 A | | |
| L08-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 26-Mar-14 A | 28-Mar-14 A | |
| L10-2018 | Remove Reshores | 2 | 0 | 26-Mar-14 A | 27-Mar-14 A | |
| P27-2004 | Shore / Form Deck | 3 | 0 | 27-Mar-14 A | 31-Mar-14 A | |
| P27-2000 | Jump/Resteel/Close Core | 4 | 0 | 29-Mar-14 A | 31-Mar-14 A | |
| P27-2006 | MEP Rough In | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2008 | ReSteel / PT Cables | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2010 | Install Edgeform/Embeds | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P26-2014 | Stress Tendons | 1 | 0 | 31-Mar-14 A | 31-Mar-14 A | |
| L09-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 31-Mar-14 A | 02-Apr-14 A | |
| P24-2016 | Strip / ReShore Deck | 3 | 0 | 01-Apr-14 A | 07-Apr-14 A | |
| L11-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 02-Apr-14 A | |
| L12-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 03-Apr-14 A | |

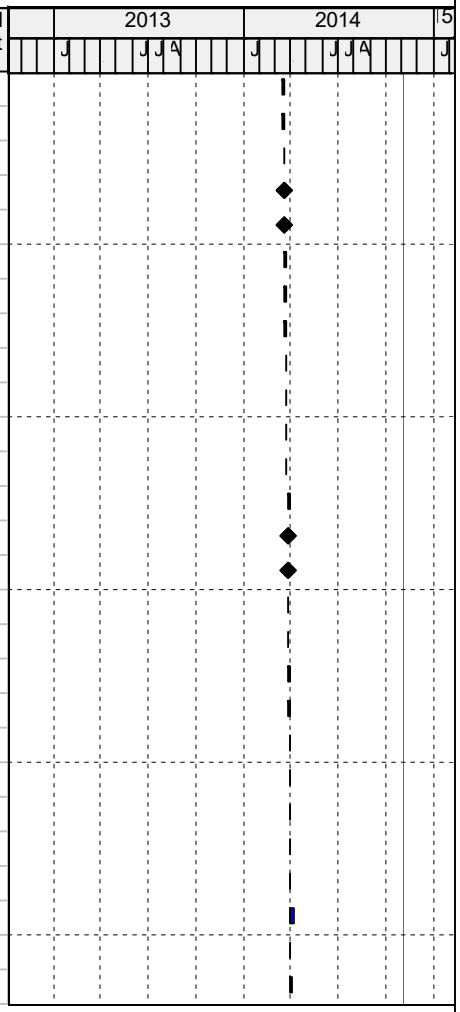


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P27-2012 | Place / Finish Deck | 0 | 0 | 02-Apr-14 A | | |
| P27-2020 | Place Conc @ Core | 0 | 0 | 02-Apr-14 A | | |
| P28-2002 | FRP Columns Below | 5 | 0 | 02-Apr-14 A | 04-Apr-14 A | |
| P28-2004 | Shore / Form Deck | 4 | 0 | 03-Apr-14 A | 08-Apr-14 A | |
| L10-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| P27-2014 | Stress Tendons | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| P25-2016 | Strip / ReShore Deck | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L14-2018 | Remove Reshores | 2 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| P28-2000 | Jump/Resteel/Close Core | 7 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| P28-2006 | MEP Rough In | 4 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2008 | ReSteel / PT Cables | 4 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Apr-14 A | 11-Apr-14 A | |
| L12-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| P28-2012 | Place / Finish Deck | 0 | 0 | 14-Apr-14 A | | |
| P28-2020 | Place Conc @ Core | 0 | 0 | 14-Apr-14 A | | |
| P29-2002 | FRP Columns Above Roof Deck | 3 | 0 | 14-Apr-14 A | 18-Apr-14 A | |
| P26-2016 | Strip / ReShore Deck | 3 | 0 | 14-Apr-14 A | 17-Apr-14 A | |
| L14-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-Apr-14 A | 18-Apr-14 A | |
| P28-2014 | Stress Tendons | 1 | 0 | 17-Apr-14 A | 17-Apr-14 A | |
| P29-2000 | Strip Core | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| P27-2016 | Strip / ReShore Deck | 3 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L15-2018 | Remove Reshores | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| P28-2016 | Strip / ReShore Deck | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L15-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L16-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-May-14 A | 19-May-14 A | |
| L16-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |

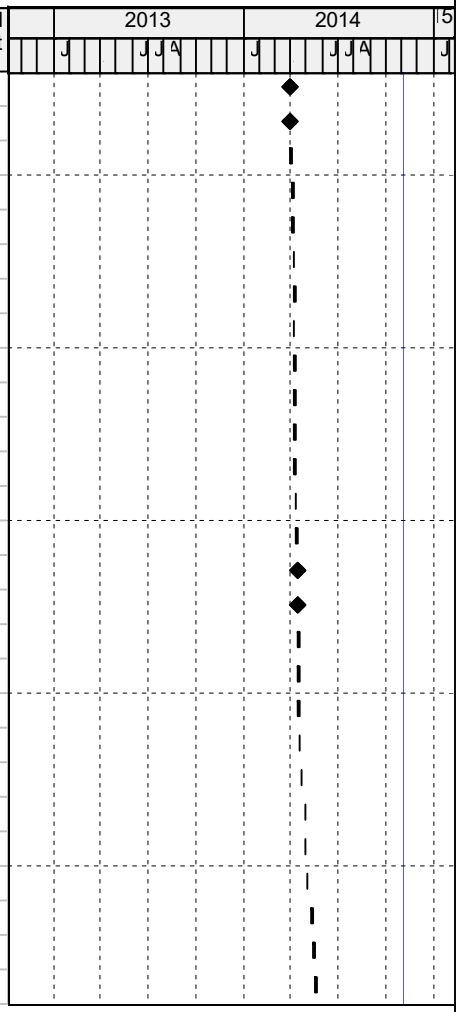


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2019 | Grind Ceiling for Skim Coat | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| **Ballroom Catwalk & Roof** | | | | | | |
| PC-2100 | Erect Structural Steel @ Porte Cochere | 3 | 0 | 30-Jan-14 A | 03-Feb-14 A | |
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 7 | 0 | 07-Feb-14 A | 17-Feb-14 A | |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| PC-2102 | Metal Decking @ Porte Cochere/ Roof | 2 | 0 | 17-Apr-14 A | 18-Apr-14 A | |
| BR-2112 | BR - Fireproofing @ Structural Steel | 2 | 0 | 27-May-14 A | 30-May-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Mech Penthouse** | | | | | | |
| PH-8706 | Set Mech Equipment @ Tower Roof | 3 | 0 | 22-May-14 A | 28-May-14 A | |
| PH-8708 | Set Equipment @ Penthouse | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| PH-8700 | PH - Structural Steel and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| **Vertical Circulation** | | | | | | |
| **Stairs** | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 25-Nov-13 A | 26-Nov-13 A | |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 27-Nov-13 A | 03-Dec-13 A | |
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 04-Dec-13 A | 05-Dec-13 A | |
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 06-Dec-13 A | 09-Dec-13 A | |
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 2 | 0 | 03-Feb-14 A | 04-Feb-14 A | |
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 2 | 0 | 06-Feb-14 A | 07-Feb-14 A | |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 2 | 0 | 07-Feb-14 A | 07-Feb-14 A | |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 2 | 0 | 07-Feb-14 A | 10-Feb-14 A | |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 2 | 0 | 10-Feb-14 A | 10-Feb-14 A | |

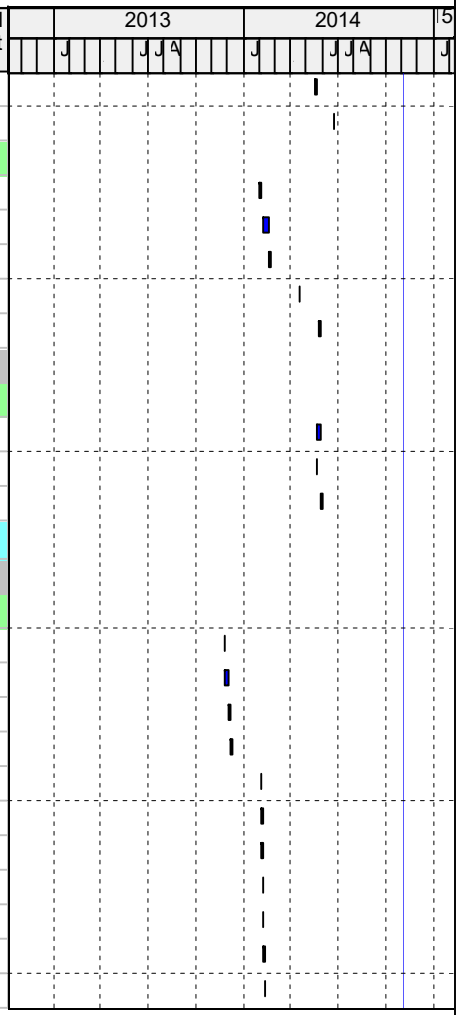



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 2 | 0 | 06-Mar-14 A | 07-Mar-14 A | |
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 2 | 0 | 07-Mar-14 A | 10-Mar-14 A | |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 2 | 0 | 13-Mar-14 A | 14-Mar-14 A | |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 2 | 0 | 08-Apr-14 A | 21-Apr-14 A | |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| S1-4040 | Stair 1 - Set Mtl Stairs / Railings L18 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 10-Dec-13 A | 11-Dec-13 A | |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 12-Dec-13 A | 13-Dec-13 A | |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 16-Dec-13 A | 17-Dec-13 A | |
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 18-Dec-13 A | 19-Dec-13 A | |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 2 | 0 | 12-Feb-14 A | 13-Feb-14 A | |
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 2 | 0 | 13-Feb-14 A | 13-Feb-14 A | |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 2 | 0 | 13-Feb-14 A | 14-Feb-14 A | |
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 2 | 0 | 19-Feb-14 A | 20-Feb-14 A | |
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 2 | 0 | 21-Feb-14 A | 24-Feb-14 A | |
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 2 | 0 | 19-Mar-14 A | 20-Mar-14 A | |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 2 | 0 | 21-Mar-14 A | 22-Mar-14 A | |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |

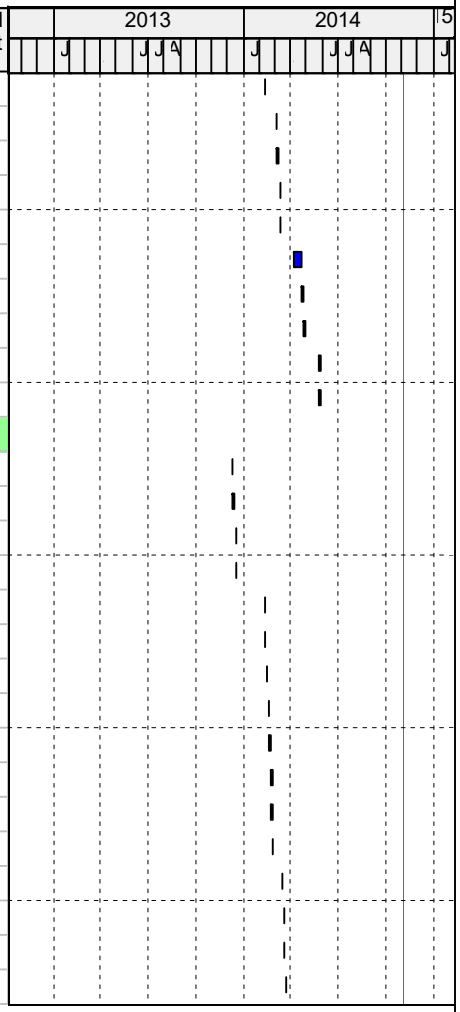



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 2 | 0 | 14-May-14 A | 15-May-14 A | |
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 2 | 0 | 16-May-14 A | 19-May-14 A | |
| S2-4038 | Stair 2 - Set Mtl Stairs / Railings L17 | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - Set Metal Stairs / Railings LL2 | 6 | 0 | 05-Mar-14 A | 20-Mar-14 A | |
| S3-4002 | Stair 3 - Set Metal Stairs / Railings LL1 | 6 | 0 | 17-Mar-14 A | 21-Mar-14 A | |
| S3-4004 | Stair 3 - Permanent Railings / Final Finishes | 4 | 4 | 11-Dec-14 | 16-Dec-14 | 22 |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |
| S4-4000 | Stair 4 - Set Metal Stairs / Railings LL2 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4002 | Stair 4 - Set Metal Stairs / Railings LL1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4004 | Stair 4 -Set Metal Stairs / Railings L1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4006 | Stair 4 - Permanent Railings / Final Finishes | 4 | 4 | 15-Dec-14 | 18-Dec-14 | 18 |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |
| S6-4000 | Stair 6 - Set Metal Stairs / Railings | 5 | 0 | 25-Jun-14 A | 01-Jul-14 A | |
| S6-4002 | Stair 6 - Permanent Railings / Final Finishes | 2 | 2 | 08-Dec-14 | 09-Dec-14 | 27 |
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes | 5 | 5 | 09-Jan-15 | 15-Jan-15 | 3 |
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a -Set Metal Stairs / Railings L1 | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| S4a-4002 | Stair 4a - Permanent Railings / Final Finishes | 2 | 2 | 19-Dec-14 | 22-Dec-14 | 18 |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 07-Jun-13 A | | |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 0 | 17-Jun-13 A | 21-Jun-13 A | |

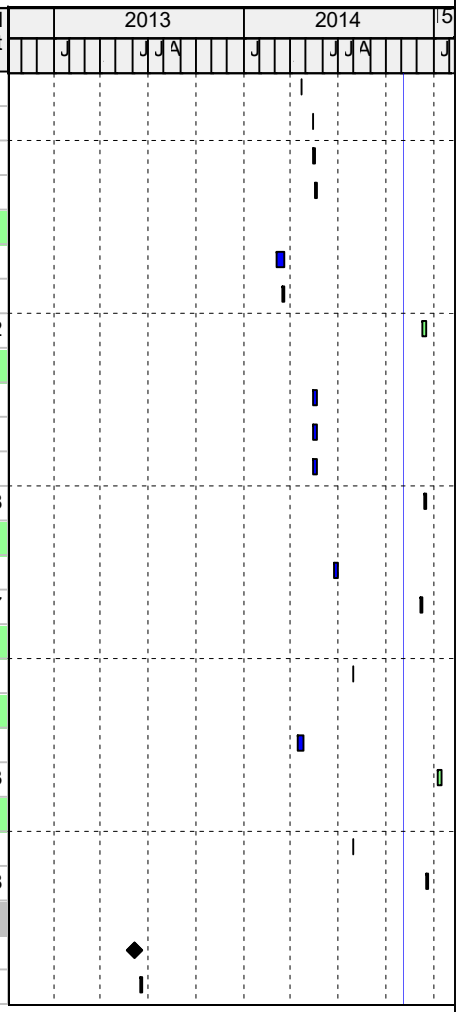



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-1004 | Elev - Submittal Approval | 21 | 0 | 21-Jun-13 A | 01-Jan-14 A | |
| EL-1006 | Elev - Release to Manufacturing | 14 | 0 | 02-Jan-14 A | 15-Jan-14 A | |
| EL-1008 | Elev - Fabrication (Engineered Geared) | 95 | 0 | 16-Jan-14 A | 14-Jun-14 A | |
| EL-1010 | Elev - Machines delivered | 1 | 0 | 12-May-14 A | 12-May-14 A | |
| EL-1011 | Elev - Elevator Machines Flown & Set At Top Of Hoist | 5 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5016 | Elev 5 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-1216 | Elev 1&2 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-3416 | Elev 3&4 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-1202 | Elev 1&2 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-3402 | Elev 3&4 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-5018 | Elev 5 - Set Hoistway Machines | 3 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| EL-1218 | Elev 1&2 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-3418 | Elev 3&4 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-1200 | Elev 1&2 - Hoistway Clear & Ready (GC) | 0 | 0 | 20-Jun-14 A | | |
| EL-1204 | Elev 1&2 - Install Rails & Brackets | 17 | 0 | 23-Jun-14 A | 15-Jul-14 A | |
| EL-3400 | Elev 3&4 - Hoistway Clear & Ready (GC) | 0 | 0 | 23-Jun-14 A | | |
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 24-Jun-14 A | | |
| EL-1206 | Elev 1&2 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Jul-14 A | |
| EL-1207 | Elev 1&2 - Install Pit Equipment/Car Sling/CWT Fram | 3 | 0 | 15-Jul-14 A | 01-Aug-14 A | |
| EL-1208 | Elev 1&2 - Install MHoist & Cable | 5 | 0 | 16-Jul-14 A | 24-Jul-14 A | |
| EL-3407 | Elev 3&4 - Install Pit Equipment/Car Sling/CWT Fram | 5 | 0 | 16-Jul-14 A | 06-Aug-14 A | |
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 21-Jul-14 A | | |
| EL-5004 | Elev 5 - Install Rails & Brackets | 13 | 0 | 21-Jul-14 A | 11-Aug-14 A | |
| EL-3404 | Elev 3&4 - Install Rails & Brackets | 18 | 0 | 23-Jul-14 A | 04-Aug-14 A | |
| EL-3406 | Elev 3&4 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 28-Jul-14 A | |

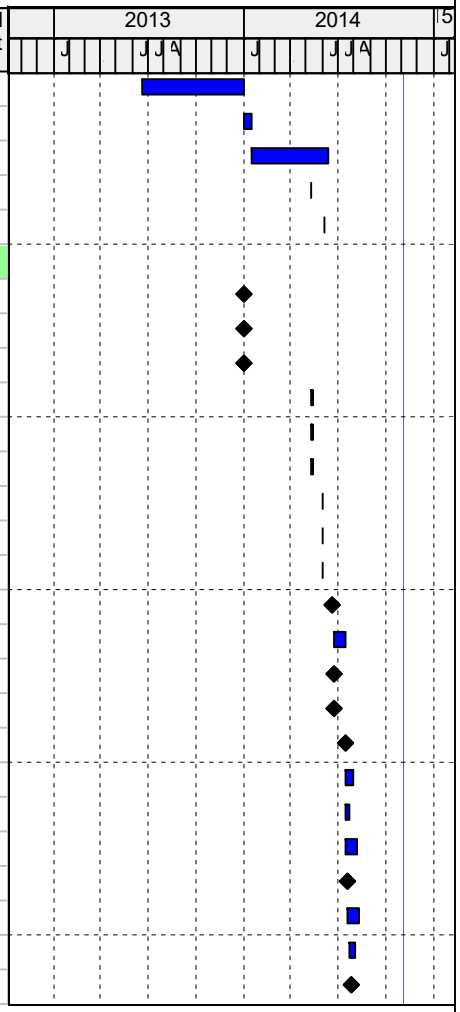


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-3408 | Elev 3&4 - Install Hoist & Cable | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| EL-5007 | Elev 5 - Install Pit Equipment/Car Sling/CWT Frame/V | 5 | 0 | 12-Aug-14 A | 15-Aug-14 A | |
| EL-1210 | Elev 1&2 - Install Entrances/Doors/Fixtures/Fascia | 19 | 0 | 14-Aug-14 A | 22-Sep-14 A | |
| EL-3410 | Elev 3&4 - Install Entrances/Doors/Fixtures/Fascia | 30 | 0 | 14-Aug-14 A | 02-Oct-14 A | |
| EL-5006 | Elev 5 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Aug-14 A | |
| EL-5008 | Elev 5 - Install MHoist & Cable | 4 | 0 | 18-Aug-14 A | 20-Aug-14 A | |
| EL-5010 | Elev 5 - Install Entrances/Doors/Fixtures/Fascia | 21 | 0 | 21-Aug-14 A | 26-Sep-14 A | |
| EL-1212 | Elev 1&2 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 22-Sep-14 A | 13-Oct-14 A | |
| EL-5012 | Elev 5 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 26-Sep-14 A | 16-Oct-14 A | |
| EL-3412 | Elev 3&4 - Install Hoistway Equipment/Pipe & Wire | 23 | 1 | 03-Oct-14 A | 03-Nov-14 | 22 |
| EL-1214 | Elev 1&2 - Install Cab/Wiring/Door Operator(s) | 11 | 0 | 14-Oct-14 A | 28-Oct-14 A | |
| EL-5014 | Elev 5 - Install Cab/Wiring/Door Operator(s) | 7 | 0 | 17-Oct-14 A | 27-Oct-14 A | |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 1 | 0 | 24-Oct-14 A | 24-Oct-14 A | |
| EL-6016 | Elev 6 - Hoistway Walls Complete (GC) | 0 | 0 | | 24-Oct-14 A | |
| EL-6004 | Elev 6 - Install Cylinders/Rails & Brackets | 4 | 0 | 27-Oct-14 A | 30-Oct-14 A | |
| EL-5022 | Elev 5 - Adjust | 5 | 1 | 28-Oct-14 A | 03-Nov-14 | 11 |
| EL-1222 | Elev 1&2 - Adjust | 5 | 2 | 29-Oct-14 A | 04-Nov-14 | 35 |
| EL-6006 | Elev 6 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 30-Oct-14 A | |
| EL-6007 | Elev 6 - Install Pit Equipment/Car Sling | 2 | 1 | 31-Oct-14 A | 03-Nov-14 | 21 |
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 3 | 3 | 04-Nov-14 | 06-Nov-14 | 11 |
| EL-3414 | Elev 3&4 - Install Cab/Wiring/Door Operator(s) | 10 | 10 | 04-Nov-14 | 17-Nov-14 | 22 |
| EL-6018 | Elev 6 - Install Machine Room Equipment | 2 | 2 | 04-Nov-14 | 05-Nov-14 | 21 |
| EL-1224 | Elev 1&2 - Clean / Paint / Punchlist | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 35 |
| EL-6010 | Elev 6 - Install Entrances/Doors/Fixtures/Fascia | 3 | 3 | 06-Nov-14 | 10-Nov-14 | 21 |
| EL-5026 | Elev 5 - Inspections | 7 | 7 | 07-Nov-14 | 13-Nov-14 | 16 |
| EL-1226 | Elev 1&2 - Inspections | 7 | 7 | 08-Nov-14 | 14-Nov-14 | 56 |
| EL-6012 | Elev 6 - Install Hoistway Equipment/Pipe & Wire | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 21 |

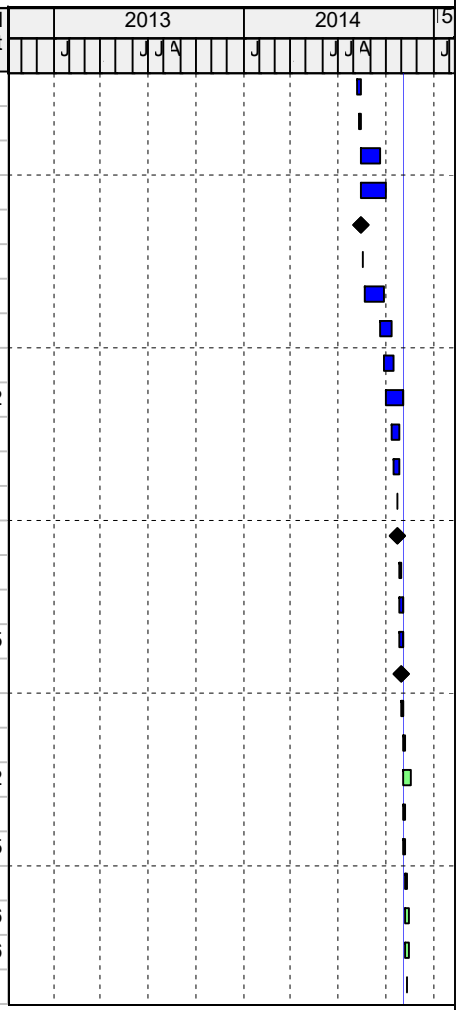


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6014 | Elev 6 - Install Cab/Wiring/Door Operator(s) | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 21 |
| EL-3422 | Elev 3&4 - Adjust | 8 | 8 | 18-Nov-14 | 01-Dec-14 | 22 |
| EL-6022 | Elev 6 - Adjust | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 21 |
| EL-6024 | Elev 6 - Clean / Paint / Punchlist | 1 | 1 | 01-Dec-14 | 01-Dec-14 | 21 |
| EL-3424 | Elev 3&4 - Clean / Paint / Punchlist | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 22 |
| EL-6026 | Elev 6 - Inspections | 1 | 1 | 02-Dec-14 | 02-Dec-14 | 33 |
| EL-3426 | Elev 3&4 - Inspections | 7 | 7 | 09-Dec-14 | 15-Dec-14 | 35 |
| **Exterior Shell** | | | | | | |
| **Elevations** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2** | | | | | | |
| L3D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Feb-14 A | 12-Feb-14 A | |
| L3-5308 | L3- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 17-Feb-14 A | 21-Feb-14 A | |
| L4D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Feb-14 A | 19-Feb-14 A | |
| L4-5308 | L4- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Feb-14 A | 28-Feb-14 A | |
| L5D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Feb-14 A | 26-Feb-14 A | |
| L5-5308 | L5- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 03-Mar-14 A | 07-Mar-14 A | |
| L6D5308 | Deliver/Stock Wall Panels | 1 | 0 | 05-Mar-14 A | 05-Mar-14 A | |
| L6-5308 | L6- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L7-5308 | L7- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L7D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Mar-14 A | 12-Mar-14 A | |
| L8D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Mar-14 A | 19-Mar-14 A | |
| L8-5308 | L8- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Mar-14 A | 28-Mar-14 A | |
| L9D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L9-5308 | L9- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 31-Mar-14 A | 07-Apr-14 A | |
| 10D5308 | Deliver/Stock Wall Panels | 1 | 0 | 02-Apr-14 A | 02-Apr-14 A | |
| L10-5308 | L10- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 07-Apr-14 A | 11-Apr-14 A | |

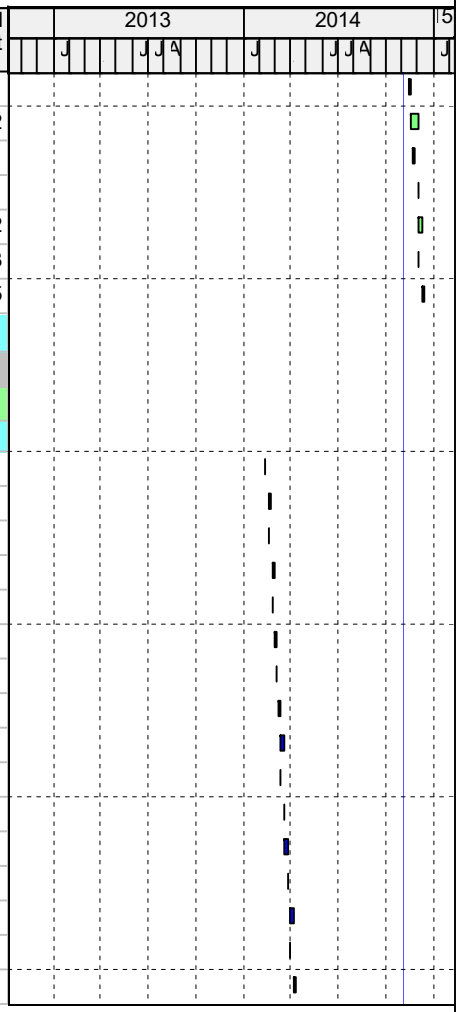



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| 11D5308 | Deliver/Stock Wall Panels | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L11-5308 | L11- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 11-Apr-14 A | 18-Apr-14 A | |
| 12D5308 | Deliver/Stock Wall Panels | 1 | 0 | 16-Apr-14 A | 16-Apr-14 A | |
| L12-5308 | L12- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Apr-14 A | 25-Apr-14 A | |
| 14D5308 | Deliver/Stock Wall Panels | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L14-5308 | L14 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Apr-14 A | 01-May-14 A | |
| 15D5308 | Deliver/Stock Wall Panels | 1 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L15-5308 | L15 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| 16D5308 | Deliver/Stock Wall Panels | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L16-5308 | L16- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| 17D5308 | Deliver/Stock Wall Panels | 1 | 0 | 14-May-14 A | 14-May-14 A | |
| L17-5308 | L17 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 20-May-14 A | 11-Jun-14 A | |
| LL2-5308 | LL2 Thru L4 - Support Frame/Sheathing for Metal Wa | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL1-5308 | LL1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| L1-5308 | L1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| **Level 1** | | | | | | |
| L3-5102 | L3- Storefront Frames | 7 | 0 | 18-Aug-14 A | 29-Sep-14 A | |
| L1-5102 | L1 - Storefront Frames (excl. Main Entry Facade) | 8 | 0 | 02-Sep-14 A | 11-Sep-14 A | |
| L1-5104 | L1 - Storefront Glazing (excl. Main Entry Facade) | 4 | 0 | 19-Sep-14 A | 24-Sep-14 A | |
| EP-5110 | L1 - Revolving Doors | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L3-5104 | L3 - Storefront Glazing | 3 | 0 | 30-Sep-14 A | 03-Oct-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Levels 3-4** | | | | | | |
| L3-5130 | L3 - Install Punch Windows | 5 | 0 | 24-Feb-14 A | 10-Mar-14 A | |
| L4-5130 | L4 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 12-Mar-14 A | |
| L5-5130 | L5 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L6-5130 | L6- Install Punch Windows | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |

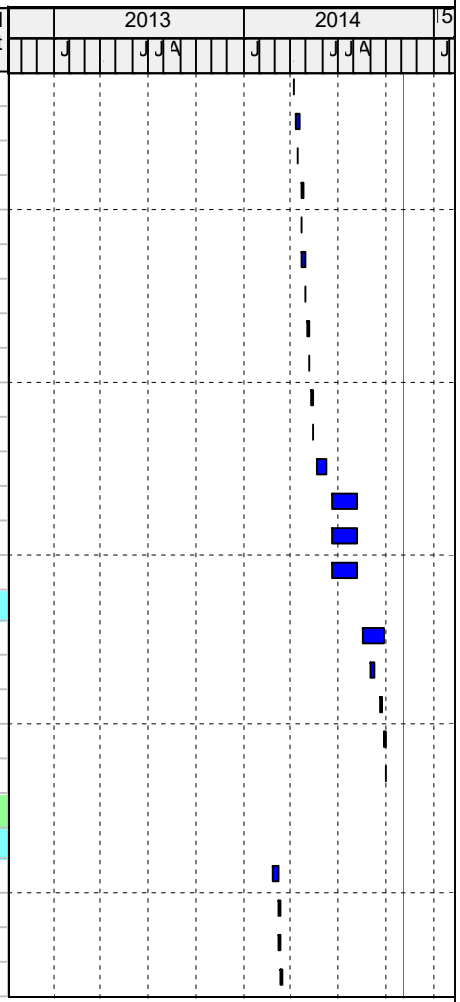



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L7-5130 | L7 - Install Punch Windows | 5 | 0 | 18-Mar-14 A | 21-Mar-14 A | |
| L8-5130 | L8 - Install Punch Windows | 5 | 0 | 24-Mar-14 A | 28-Mar-14 A | |
| L9-5130 | L9 - Install Punch Windows | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L10-5130 | L10 - Install Punch Windows | 5 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-5130 | L11 - Install Punch Windows | 5 | 0 | 14-Apr-14 A | 21-Apr-14 A | |
| L12-5130 | L12 - Install Punch Windows | 5 | 0 | 22-Apr-14 A | 25-Apr-14 A | |
| L14-5130 | L14 - Install Punch Windows | 5 | 0 | 28-Apr-14 A | 05-May-14 A | |
| L15-5130 | L15 - Install Punch Windows | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| L16-5130 | L16 - Install Punch Windows | 5 | 0 | 12-May-14 A | 20-May-14 A | |
| L17-5130 | L17 - Install Punch Windows | 5 | 0 | 27-May-14 A | 16-Jun-14 A | |
| Roofs | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| RF-4026 | L1 - City Park - Protection Board | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| **Pool Membrane - (elev 18')** | | | | | | |
| RF-4034 | Pool - Install plumbing | 3 | 0 | 20-Oct-14 A | 22-Oct-14 A | |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |
| RF-4010 | AR - Set Mechanical Equipment | 5 | 0 | 10-Jun-14 A | 12-Jun-14 A | |
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 10 | 0 | 04-Aug-14 A | 27-Aug-14 A | |
| RF-4012 | L2.5 Horseshoe - Install corrugated metal panels | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 8 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |
| PC-4008 | RF - Entry / Porte Cochere Roofing System | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | RF - Upper Ballroom Roofing System | 3 | 0 | 28-Jul-14 A | 31-Jul-14 A | |

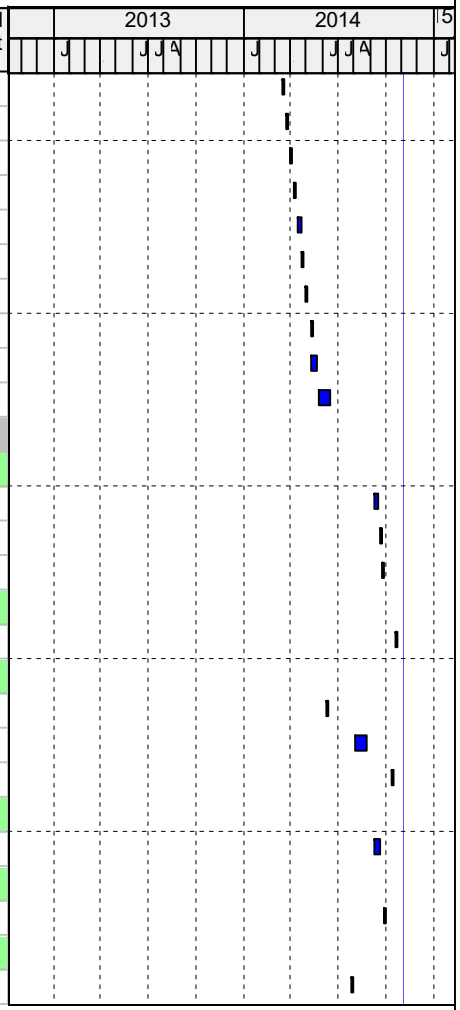



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 4 | 0 | 31-Jul-14 A | 04-Aug-14 A | |
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |
| RF-4018 | TR - Terrace Roof - Green Roofing System | 5 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| RF-4020 | TR - Terrace Roof - Install sheet metal capping | 1 | 1 | 20-Nov-14 | 20-Nov-14 | 27 |
| RF-4022 | TR - Terrace Roof - Install deocrative metal railing | 3 | 3 | 21-Nov-14 | 25-Nov-14 | 27 |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Perimeter Framing / Sul | 10 | 0 | 02-Jun-14 A | 08-Jul-14 A | |
| RF-4002 | Tower Roof - Roofing System | 10 | 0 | 20-Aug-14 A | 17-Sep-14 A | |
| **PH - Roof - (elev 173')** | | | | | | |
| RF-4030 | PH - Roofing System | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| RF-4032 | PH - Coping / Flashing [DELETED] | 3 | 0 | 01-Sep-14 A | 01-Sep-14 A | |
| **Rough-In's** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6002 | LL4 - Layout | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| LL4-6008 | LL4 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL4-6012 | LL4 - Fire Sprinkler Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6014 | LL4 - Plumbing Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6018 | LL4 - HVAC Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6004 | LL4 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL4-6016 | LL4 - Electrical Rl | 10 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties Rl | 8 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6010 | LL4 - Elevator pits | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| LL4-6020 | LL4 - H Mtl Frames | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL4-6024 | LL4 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |

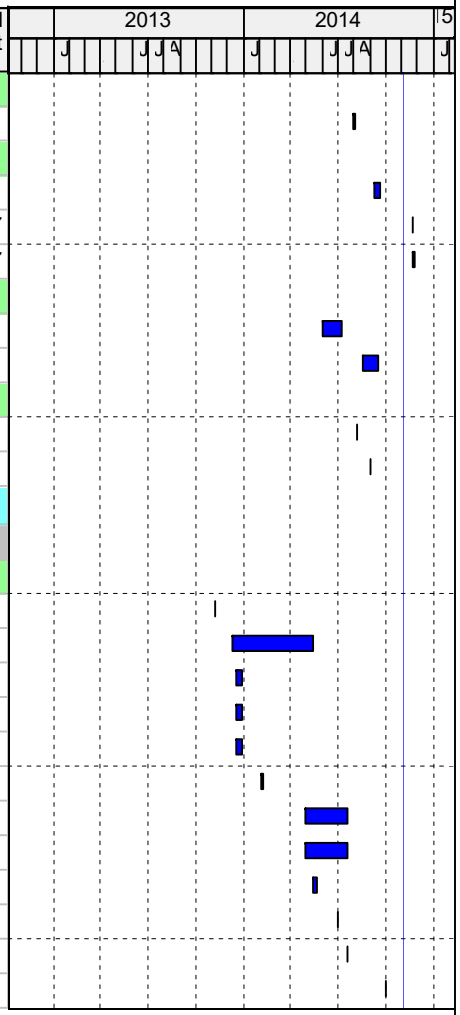



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6002 | LL3 - Layout | 1 | 0 | 19-Nov-13 A | 19-Nov-13 A | |
| LL3-6008 | LL3 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL3-6012 | LL3 - Fire Sprinkler RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6014 | LL3 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6018 | LL3 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6004 | LL3 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL3-6020 | LL3 - H Mtl Frames | 3 | 0 | 08-May-14 A | 09-May-14 A | |
| LL3-6010 | LL3 - F/P Curbs | 5 | 0 | 19-May-14 A | 19-May-14 A | |
| LL3-6016 | LL3 - Electrical RI | 2 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties RI | 8 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL3-6024 | LL3 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6002 | LL2 - Layout | 1 | 0 | 14-Jan-14 A | 14-Jan-14 A | |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| LL2-6012 | LL2 - Fire Sprinkler RI | 10 | 0 | 21-Jan-14 A | 03-Feb-14 A | |
| LL2-6014 | LL2 - Plumbing RI | 10 | 0 | 21-Jan-14 A | 14-Feb-14 A | |
| LL2E-6016 | LL2 - Electrical RI | 8 | 0 | 03-Feb-14 A | 17-Mar-14 A | |
| LL2-6016 | LL2 - Electrical RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2-6018 | LL2 - HVAC RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2–6004 | LL2 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL2E-6004 | LL2 - CMU Walls | 10 | 0 | 04-Mar-14 A | 09-May-14 A | |
| LL2E-6012 | LL2 - Fire Sprinkler RI | 8 | 0 | 21-Mar-14 A | 01-Apr-14 A | |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 24-Apr-14 A | |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 3 | 0 | 23-Apr-14 A | 21-Jul-14 A | |
| LL2E-6020 | LL2 - H Mtl Frames | 3 | 0 | 09-May-14 A | 12-May-14 A | |

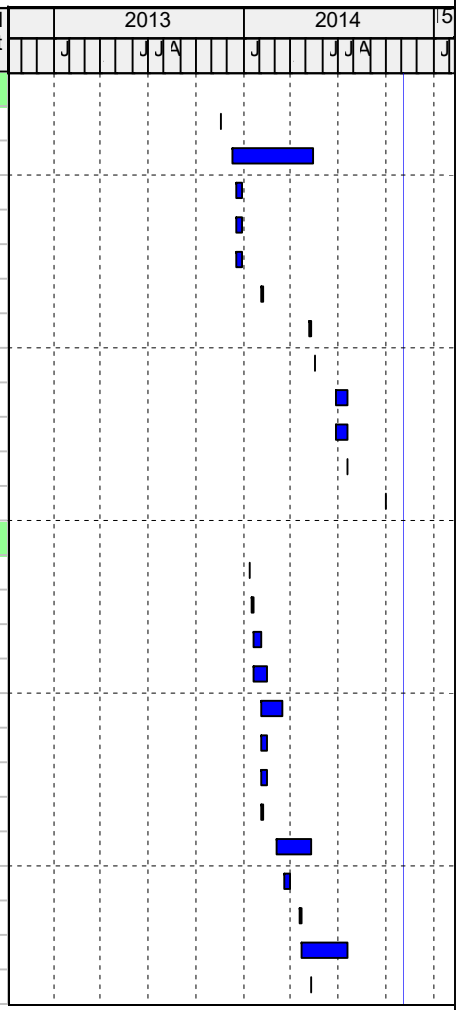



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-6020 | LL2 - H Mtl Frames | 3 | 0 | 12-May-14 A | 13-May-14 A | |
| LL2E-6008 | LL2 - Int Wall Framing | 5 | 0 | 13-May-14 A | 22-Jun-14 A | |
| LL2E-6014 | LL2 - Plumbing RI | 8 | 0 | 13-May-14 A | 30-May-14 A | |
| LL2E-6018 | LL2 - HVAC RI | 8 | 0 | 13-May-14 A | 04-Aug-14 A | |
| LL2E-6022 | LL2 - Fire Alarm / Elec Specialties RI (East of 10) | 8 | 0 | 13-May-14 A | 22-Sep-14 A | |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties RI (West of 10) | 8 | 0 | 19-May-14 A | 22-Sep-14 A | |
| LL2-6015 | LL2 - Main Elect Room Set Equip / RI - Power to Ma | 15 | 0 | 30-Jun-14 A | 26-Sep-14 A | |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 0 | 16-Jul-14 A | 21-Jul-14 A | |
| LL2-6024 | LL2 - Inspections | 2 | 0 | 15-Sep-14 A | 03-Oct-14 A | |
| LL2-6010 | LL2 - F/P Curbs @ Parking | 4 | 4 | 03-Nov-14 | 06-Nov-14 | 37 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6002 | Layout | 3 | 0 | 03-Jan-14 A | 08-Jan-14 A | |
| LL1-6008 | Int Wall Framing & Inspection | 6 | 0 | 08-Jan-14 A | 21-Jul-14 A | |
| LL1-Z2-6002 | Layout | 3 | 0 | 08-Jan-14 A | 14-Jan-14 A | |
| LL1-Z3-6002 | Layout | 3 | 0 | 14-Jan-14 A | 17-Jan-14 A | |
| LL1-Z2-6008 | Int Wall Framing & Inspection | 6 | 0 | 17-Jan-14 A | 01-Aug-14 A | |
| LL1-Z3-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-Jan-14 A | 04-Aug-14 A | |
| LL1-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 09-May-14 A | |
| LL1-Z2-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 28-Apr-14 A | |
| LL1-Z3-6004 | CMU Walls (At All Areas North of Q-Line) | 3 | 0 | 03-Feb-14 A | 13-May-14 A | |
| LL1C-6012 | Complete Fire Sprinkler RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6016 | Complete Electrical RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 10 | 0 | 17-Feb-14 A | 16-Sep-14 A | |
| LL1C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 30-Apr-14 A | |

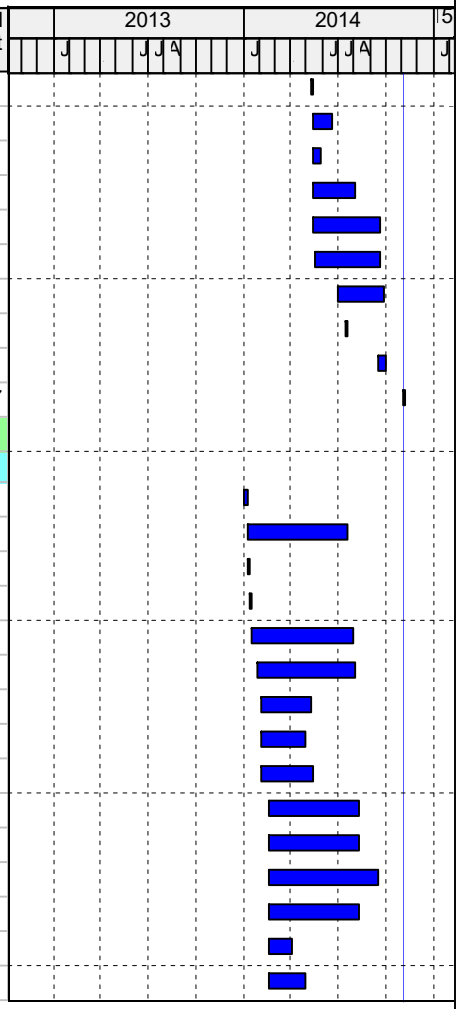



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-Z2-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z2-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z3-6012 | Fire Sprinkler RI (At All Areas North of Q-Line) | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z3-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 11-Sep-14 A | |
| LL1-Z3-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z2C-6012 | Complete Fire Sprinkler RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6014 | Complete Plumbing RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6016 | Complete Electrical RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 15 | 0 | 24-Feb-14 A | 15-Sep-14 A | |
| LL1-Z2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2-6020 | Hollow Metal Door Frames | 5 | 0 | 17-Mar-14 A | 04-Apr-14 A | |
| LL1-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| LL1-Z3-6020 | Hollow Metal Door Frames (At All Areas North of Q-Lir | 1 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| L1B-6004 | CMU Walls [including East Service Corridor] | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L1L-6002 | Layout [including back of house] | 3 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 29-Apr-14 A | |
| L1B-6008 | Int Wall Framing & Inspection | 6 | 0 | 21-Apr-14 A | 08-Aug-14 A | |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 5 | 0 | 25-Apr-14 A | 21-Jul-14 A | |
| LL1C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 30-Apr-14 A | 30-Apr-14 A | |

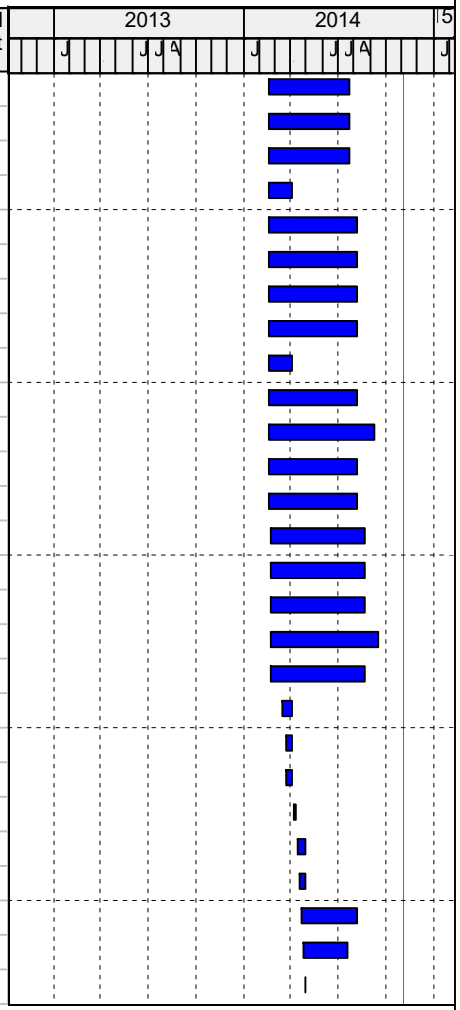


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-6004 | CMU Walls [including public restroom] | 3 | 0 | 05-May-14 A | 08-May-14 A | |
| L1K-6002 | Layout [including public restroom] | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| L1K-6008 | Int Wall Framing & Inspection | 4 | 0 | 09-May-14 A | 22-Aug-14 A | |
| L1B-6002 | Layout [including East Service Corridor] | 3 | 0 | 14-May-14 A | 27-May-14 A | |
| L1L-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-May-14 A | 06-Oct-14 A | |
| L1L-6004 | CMU Walls [including back of house] | 3 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L1K-6012 | Fire Sprinkler RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6014 | Plumbing RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6016 | Electrical RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1K-6018 | HVAC RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1B-6014 | Plumbing RI [including East Service Corridor] | 10 | 0 | 16-Jun-14 A | 24-Jun-14 A | |
| L1B-6018 | HVAC RI | 10 | 0 | 20-Jun-14 A | 15-Aug-14 A | |
| L1B-6012 | Fire Sprinkler RI | 10 | 0 | 21-Jun-14 A | 15-Aug-14 A | |
| L1L-6018 | HVAC RI | 5 | 0 | 23-Jun-14 A | 13-Oct-14 A | |
| L1L-6014 | Plumbing RI | 5 | 0 | 24-Jun-14 A | 28-Oct-14 A | |
| L1L-6010 | CMU Seismic Clips [including back of house] [DELET | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1L-6012 | Fire Sprinkler RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |
| L1L-6016 | Electrical RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |
| L1L-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 27-Jun-14 A | 13-Oct-14 A | |
| L1K-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 27-Jun-14 A | 29-Sep-14 A | |
| LL1-Z3-6009 | Frame Ceilings [DELETED] | 4 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1B-6016 | Electrical RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| L1B-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| LL1-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-Z2-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L1B-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-6024 | Inspections for Cover | 1 | 0 | 23-Jul-14 A | 24-Jul-14 A | |

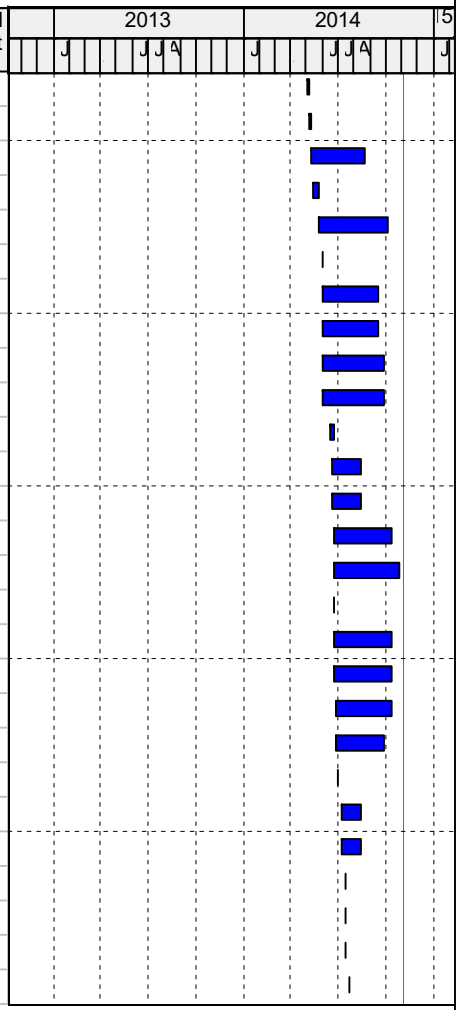


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-6020 | Hollow Metal Door Frames | 5 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| LL1-Z3-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L1K-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 06-Aug-14 A | |
| LL1-Z2-6024 | Inspections for Cover | 2 | 0 | 07-Aug-14 A | 08-Aug-14 A | |
| L1K-6020 | Hollow Metal Door Frames | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-Z2-6009 | Frame Ceilings & Inspection | 6 | 0 | 22-Aug-14 A | 13-Oct-14 A | |
| L1L-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Aug-14 A | 13-Oct-14 A | |
| LL1-6009 | Frame Ceilings & Inspection (except for bar redesign | 9 | 0 | 02-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3-6024 | Inspections for Cover | 2 | 0 | 12-Sep-14 A | 12-Sep-14 A | |
| LL1-Z3C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6016 | Complete Electrical RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3C-6018 | Complete HVAC RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| L1KC-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 4 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L1B-6024 | Inspections for Cover (Main Ballroom N/S/W Walls & | 3 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1K-6024 | Inspections for Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1KC-6014 | Complete Plumbing RI @ Ceilings & Inspection | 4 | 0 | 02-Oct-14 A | 07-Oct-14 A | |
| L1BC-6014 | Complete Plumbing RI @ Ceilings | 7 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L1BC-6018 | Complete HVAC RI @ Ceilings | 7 | 1 | 06-Oct-14 A | 03-Nov-14 | 19 |
| L1KC-6018 | Complete HVAC RI @ Ceilings & Inspection | 4 | 2 | 06-Oct-14 A | 05-Nov-14 | 10 |
| L1KC-6016 | Complete Electrical RI @ Ceilings & Inspection | 3 | 1 | 20-Oct-14 A | 04-Nov-14 | 11 |
| L1KC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 3 | 1 | 20-Oct-14 A | 04-Nov-14 | 11 |
| L1L-6024 | Inspections for Cover | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L1B-6009 | Frame Ceilings | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 9 |
| L1BC-6012 | Complete Fire Sprinkler RI @ Ceilings | 6 | 6 | 03-Nov-14 | 10-Nov-14 | 14 |
| L1K-6009 | Frame Ceilings [public restroom] | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 10 |

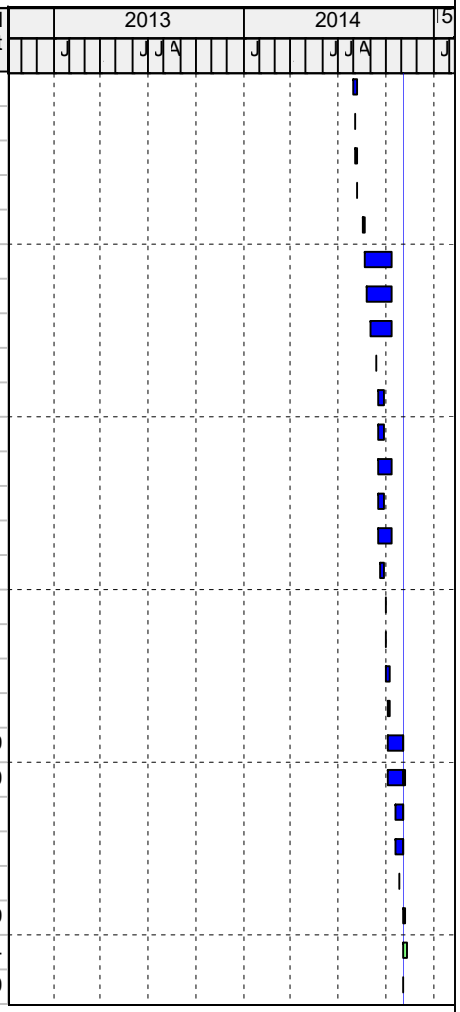



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1BC-6016 | Complete Electrical RI @ Ceilings & Inspection | 6 | 6 | 10-Nov-14 | 17-Nov-14 | 9 |
| L1BC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 6 | 6 | 10-Nov-14 | 17-Nov-14 | 9 |
| L1L-6009 | Frame Ceilings & Inspection | 13 | 13 | 17-Nov-14 | 05-Dec-14 | 1 |
| L1LC-6012 | Complete Fire Sprinkler RI @ Ceilings | 4 | 4 | 17-Nov-14 | 20-Nov-14 | 1 |
| L1LC-6014 | Complete Plumbing RI @ Ceilings | 4 | 4 | 17-Nov-14 | 20-Nov-14 | 1 |
| L1LC-6016 | Complete Electrical RI @ Ceilings | 4 | 4 | 17-Nov-14 | 20-Nov-14 | 1 |
| L1LC-6018 | Complete HVAC RI @ Ceilings | 4 | 4 | 17-Nov-14 | 20-Nov-14 | 1 |
| L1LC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 4 | 4 | 17-Nov-14 | 20-Nov-14 | 1 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 0 | 17-Apr-14 A | 09-May-14 A | |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6006 | L2 - Support Frame/Sheathing for Metal Panels | 6 | 0 | 23-Apr-14 A | 07-Aug-14 A | |
| L02-6008 | L2 - Int Wall Framing | 10 | 0 | 25-Apr-14 A | 17-Jul-14 A | |
| L02-6014 | L2 - Plumbing RI | 15 | 0 | 28-Apr-14 A | 07-Aug-14 A | |
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 0 | 28-Apr-14 A | 09-May-14 A | |
| L02-6004 | L2 - CMU Walls | 5 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L02-6002 | L2 - Layout | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L02-6018 | L2 - HVAC RI (including equipment) | 20 | 0 | 18-Jun-14 A | 10-Sep-14 A | |
| L02-6016 | L2 - Electrical RI | 10 | 0 | 24-Jun-14 A | 14-Aug-14 A | |
| L02-6022 | L2 - Fire Alarm / Elec Specialties RI | 10 | 0 | 24-Jun-14 A | 10-Oct-14 A | |
| L02-6012 | L2 - Fire Sprinkler RI | 10 | 0 | 26-Jun-14 A | 07-Aug-14 A | |
| L02-6020 | L2 - H Mtl Frames | 5 | 0 | 11-Jul-14 A | 17-Jul-14 A | |
| L02-6024 | L2 - Inspections - North Half | 2 | 0 | 10-Oct-14 A | 20-Oct-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L07-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 01-Apr-11 A | 11-Apr-11 A | |

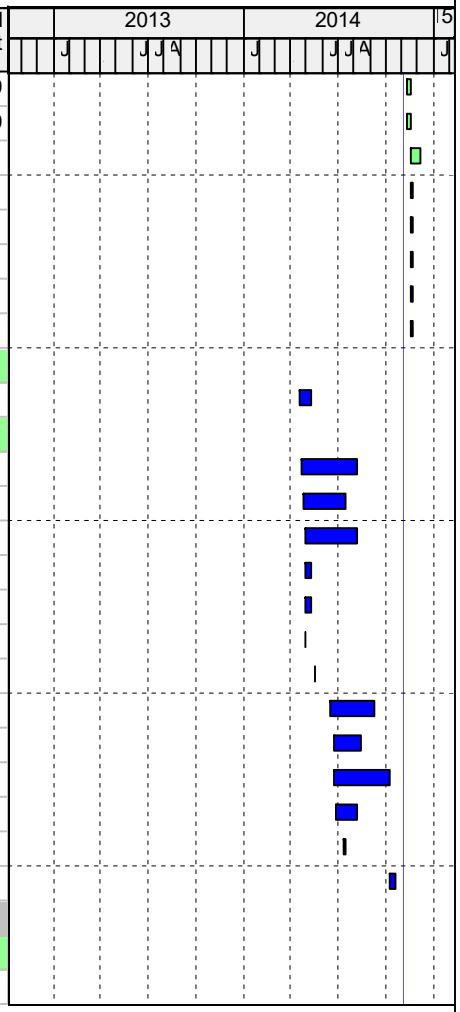



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6012 | Fire Sprinkler Mains | 5 | 0 | 01-Feb-14 A | 03-Apr-14 A | |
| L03-8219 | HVAC Risers | 5 | 0 | 11-Feb-14 A | 23-Mar-14 A | |
| L03-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 11-Feb-14 A | 03-Mar-14 A | |
| L03-6002 | Layout | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| L04-8219 | HVAC Risers | 5 | 0 | 13-Feb-14 A | 23-Mar-14 A | |
| L05-8219 | HVAC Risers | 5 | 0 | 17-Feb-14 A | 03-Mar-14 A | |
| L03-6008 | Frame Shaft Walls | 3 | 0 | 18-Feb-14 A | 26-Mar-14 A | |
| L04-6002 | Layout | 5 | 0 | 19-Feb-14 A | 25-Feb-14 A | |
| L04-6008 | Frame Shaft Walls | 3 | 0 | 20-Feb-14 A | 26-Mar-14 A | |
| L03-6011 | PreRock Shafts | 2 | 0 | 24-Feb-14 A | 25-Mar-14 A | |
| L03-6010 | Frame Walls | 5 | 0 | 25-Feb-14 A | 25-Mar-14 A | |
| L05-6002 | Layout | 5 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| L04-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 28-Feb-14 A | 05-Mar-14 A | |
| L03-6016 | Electrical RI | 5 | 0 | 03-Mar-14 A | 04-Apr-14 A | |
| L03-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 12-Mar-14 A | |
| L04-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 13-Mar-14 A | |
| L04-6010 | Frame Walls | 5 | 0 | 04-Mar-14 A | 05-Jun-14 A | |
| L05-6008 | Frame Shaft Walls | 3 | 0 | 05-Mar-14 A | 27-Mar-14 A | |
| L06-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L07-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L05-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 06-Mar-14 A | 21-Mar-14 A | |
| L03-6020 | Install Hollow Metal Frames | 3 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L04-6020 | Install Hollow Metal Frames | 3 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L05-6010 | Frame Walls | 5 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L06-6002 | Layout | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L04-6011 | PreRock Shafts | 2 | 0 | 18-Mar-14 A | 25-Mar-14 A | |
| L05-6009 | Inspect Shafts | 1 | 0 | 18-Mar-14 A | 18-Mar-14 A | |

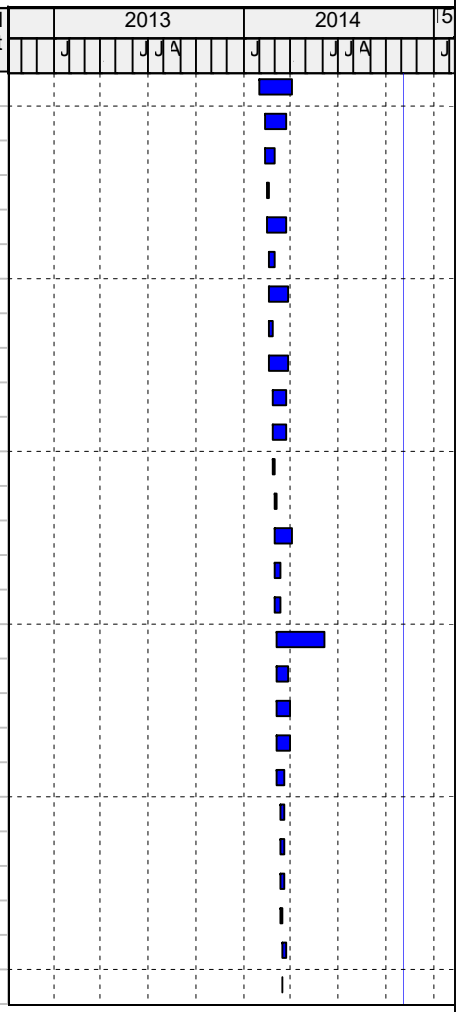


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| L06-6008 | Frame Shaft Walls | 3 | 0 | 19-Mar-14 A | 03-Apr-14 A | |
| L06-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 27-Mar-14 A | |
| L04-6016 | Electrical RI | 5 | 0 | 20-Mar-14 A | 09-Apr-14 A | |
| L05-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 26-Mar-14 A | |
| L06-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 07-Apr-14 A | |
| L07-6002 | Layout | 5 | 0 | 24-Mar-14 A | 30-Apr-14 A | |
| L03-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L03-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L05-6016 | Electrical RI | 5 | 0 | 25-Mar-14 A | 05-Jun-14 A | |
| L04-6019 | Complete Top Out GWB | 2 | 0 | 26-Mar-14 A | 06-Jun-14 A | |
| L05-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L06-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| L03-6019 | Complete Top Out GWB | 2 | 0 | 27-Mar-14 A | 02-May-14 A | |
| L08-6002 | Layout | 5 | 0 | 27-Mar-14 A | 02-Apr-14 A | |
| L05-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 28-Mar-14 A | 03-Apr-14 A | |
| L06-6010 | Frame Walls | 5 | 0 | 28-Mar-14 A | 07-Apr-14 A | |
| L03-6012 | Fire Sprinkler Mains | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L07-6008 | Frame Shaft Walls | 3 | 0 | 31-Mar-14 A | 03-Apr-14 A | |
| L05-6019 | Complete Top Out GWB | 2 | 0 | 01-Apr-14 A | 08-Apr-14 A | |
| L08-6008 | Frame Shaft Walls | 3 | 0 | 02-Apr-14 A | 21-Apr-14 A | |
| L03-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L04-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L05-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L06-6016 | Electrical RI | 5 | 0 | 03-Apr-14 A | 15-Apr-14 A | |

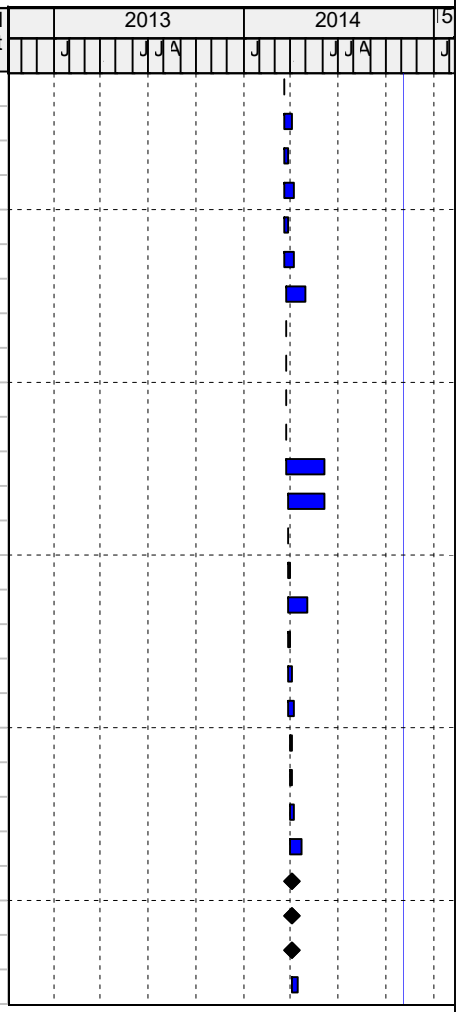


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6009 | Inspect Shafts | 1 | 0 | 03-Apr-14 A | 03-Apr-14 A | |
| L07-6011 | PreRock Shafts | 2 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| L05-6012 | Fire Sprinkler Mains | 5 | 0 | 04-Apr-14 A | 30-Apr-14 A | |
| L06-6012 | Fire Sprinkler Mains | 5 | 0 | 07-Apr-14 A | 30-Apr-14 A | |
| L06-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L06-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L07-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| L07-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L03-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L03-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L04-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L06-6009 | Inspect Shafts | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L06-6019 | Complete Top Out GWB | 2 | 0 | 08-Apr-14 A | 18-Apr-14 A | |
| L07-6010 | Frame Walls | 5 | 0 | 08-Apr-14 A | 15-Apr-14 A | |
| L08-6011 | PreRock Shafts | 2 | 0 | 08-Apr-14 A | 23-Apr-14 A | |
| L09-6002 | Layout | 5 | 0 | 08-Apr-14 A | 26-Apr-14 A | |
| L03-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 09-Apr-14 A | 08-May-14 A | |
| L03-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L05-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 09-Apr-14 A | 14-Apr-14 A | |
| L08-6009 | Inspect Shafts | 1 | 0 | 09-Apr-14 A | 25-Apr-14 A | |
| L09-6008 | Frame Shaft Walls | 3 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| L08-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| L04-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 15-Apr-14 A | 16-Apr-14 A | |
| L07-6012 | Fire Sprinkler Mains | 5 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| L07-6016 | Electrical RI | 5 | 0 | 15-Apr-14 A | 12-May-14 A | |
| L07-6020 | Install Hollow Metal Frames | 3 | 0 | 16-Apr-14 A | 23-Apr-14 A | |
| L05-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 17-Apr-14 A | 25-Apr-14 A | |

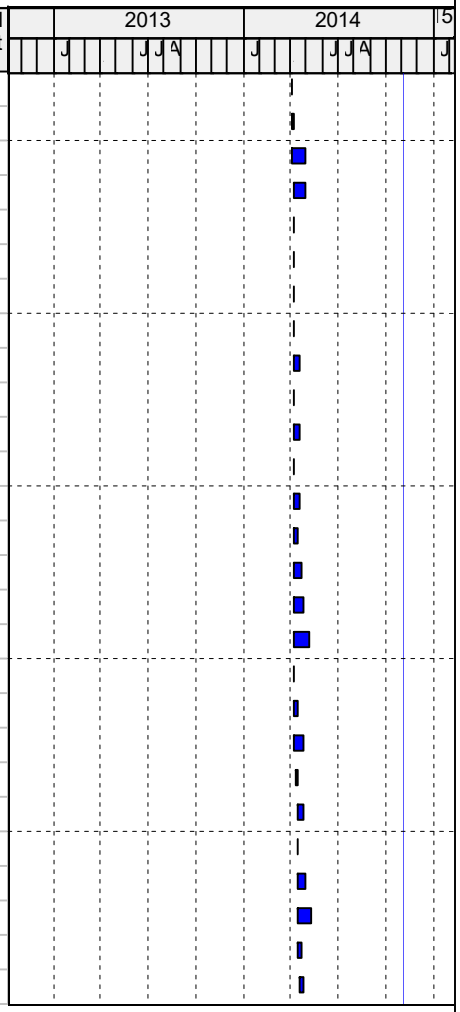



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 17-Apr-14 A | 12-May-14 A | |
| L06-6023 | Inspection of Exterior Framing | 0 | 0 | 17-Apr-14 A | | |
| L09-8219 | HVAC Risers | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L09-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L04-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 18-Apr-14 A | 20-Apr-14 A | |
| L04-6028 | PreRock at Heat Pumps | 2 | 0 | 20-Apr-14 A | 22-Apr-14 A | |
| L08-8219 | HVAC Risers | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6009 | Inspect Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6011 | PreRock Shafts | 2 | 0 | 22-Apr-14 A | 24-Apr-14 A | |
| L04-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L06-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 23-Apr-14 A | 25-Apr-14 A | |
| L08-6020 | Install Hollow Metal Frames | 3 | 0 | 23-Apr-14 A | 13-May-14 A | |
| L11-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L11-8220 | Plumbing Risers - Install | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L04-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L09-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L10-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L10-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 20-May-14 A | |
| L12-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L04-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 25-Apr-14 A | 11-Jun-14 A | |
| L04-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L09-6010 | Frame Walls | 5 | 0 | 25-Apr-14 A | 20-May-14 A | |
| L09-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L10-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L11-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 30-Apr-14 A | |

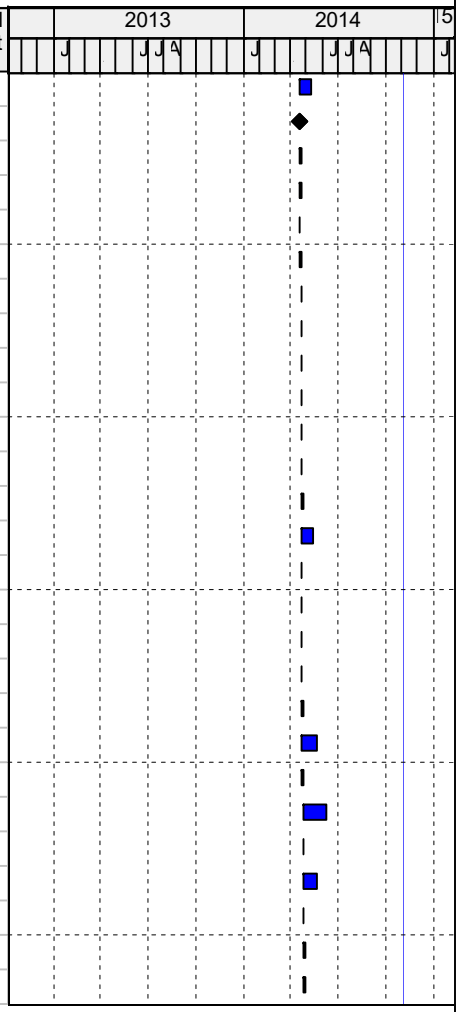



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L08-6010 | Frame Walls | 5 | 0 | 26-Apr-14 A | 30-Apr-14 A | |
| L10-6002 | Layout | 5 | 0 | 27-Apr-14 A | 27-Apr-14 A | |
| L04-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 28-Apr-14 A | 30-Apr-14 A | |
| L05-6018 | HVAC RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6028 | PreRock at Heat Pumps | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L07-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 28-Apr-14 A | 12-May-14 A | |
| L10-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-Apr-14 A | 22-May-14 A | |
| L11-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L12-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L05-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| L05-6028 | PreRock at Heat Pumps | 2 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L06-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 09-May-14 A | |
| L06-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L06-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L08-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L08-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L09-6020 | Install Hollow Metal Frames | 3 | 0 | 29-Apr-14 A | 20-May-14 A | |
| L09-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |

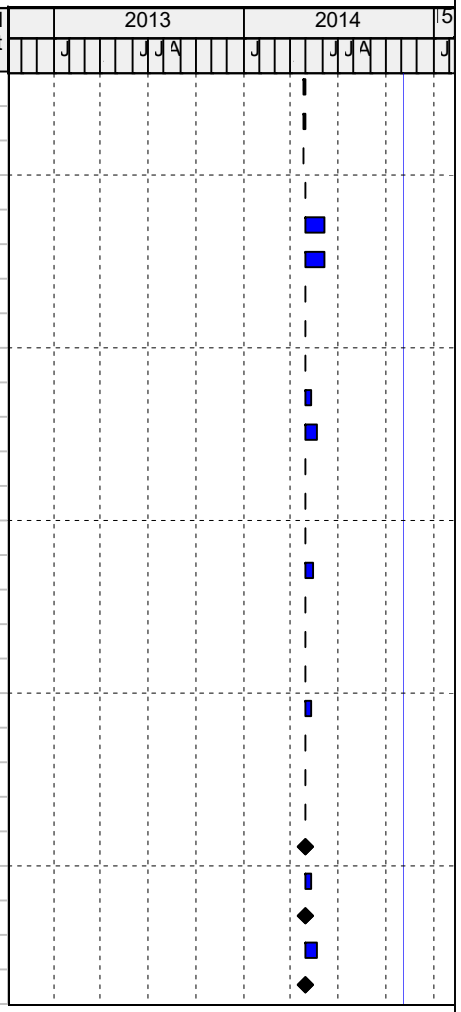



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L04-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 30-Apr-14 A | 02-May-14 A | |
| L09-6019 | Complete Top Out GWB | 2 | 0 | 30-Apr-14 A | 06-Jun-14 A | |
| L11-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L12-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L03-6028 | PreRock at Heat Pumps | 2 | 0 | 01-May-14 A | 02-May-14 A | |
| L05-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L06-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L03-6014 | Set Tubs & Plumbing RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L05-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L05-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| L06-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L06-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 09-May-14 A | |
| L03-6018 | HVAC RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L03-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 06-May-14 A | 06-May-14 A | |
| L07-6014 | Set Tubs & Plumbing RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L07-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 06-May-14 A | 09-May-14 A | |
| L03-6004 | CMU Wall/Clips | 3 | 0 | 07-May-14 A | 08-May-14 A | |
| L03-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L03-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 08-May-14 A | 13-May-14 A | |
| L03-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6004 | CMU Walls | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6018 | HVAC RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |

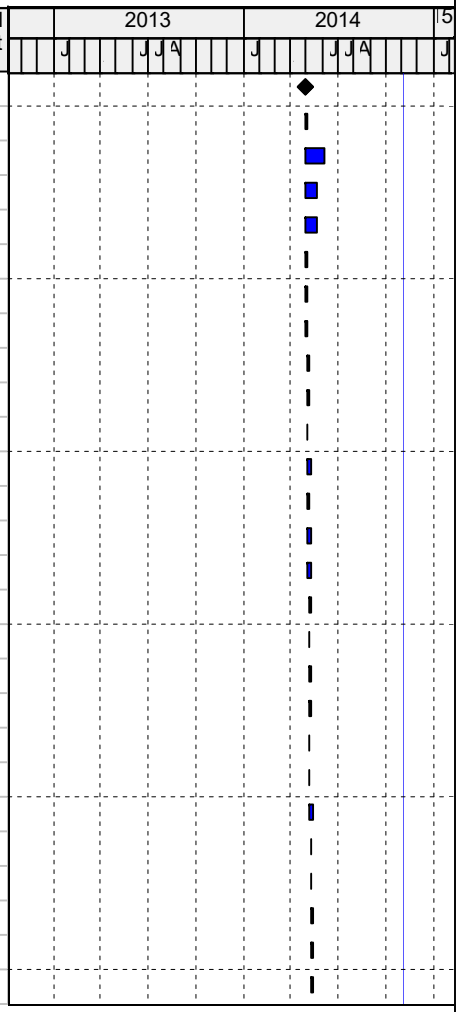



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L11-6010 | Frame Walls | 5 | 0 | 09-May-14 A | 15-May-14 A | |
| L05-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 12-May-14 A | 05-Jun-14 A | |
| L07-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 12-May-14 A | 13-May-14 A | |
| L11-6020 | Install Hollow Metal Frames | 3 | 0 | 12-May-14 A | 14-May-14 A | |
| L11-6019 | Complete Top Out GWB | 2 | 0 | 12-May-14 A | 14-May-14 A | |
| L14-6002 | Layout | 5 | 0 | 12-May-14 A | 14-May-14 A | |
| L15-6002 | Layout | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L05-6004 | CMU Walls | 3 | 0 | 13-May-14 A | 13-May-14 A | |
| L06-6018 | HVAC Rl | 5 | 0 | 13-May-14 A | 25-Jun-14 A | |
| L06-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 13-May-14 A | 14-Jul-14 A | |
| L07-6018 | HVAC Rl | 5 | 0 | 13-May-14 A | 05-Jun-14 A | |
| L07-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| L07-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 13-May-14 A | 13-May-14 A | |
| L14-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L16-6002 | Layout | 5 | 0 | 13-May-14 A | 16-May-14 A | |
| L06-6004 | CMU Walls | 3 | 0 | 14-May-14 A | 14-May-14 A | |
| L07-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 15-May-14 A | |
| L08-6012 | Fire Sprinkler Mains | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6002 | Layout | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L07-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 16-May-14 A | 25-Jun-14 A | |
| L08-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-May-14 A | 16-May-14 A | |

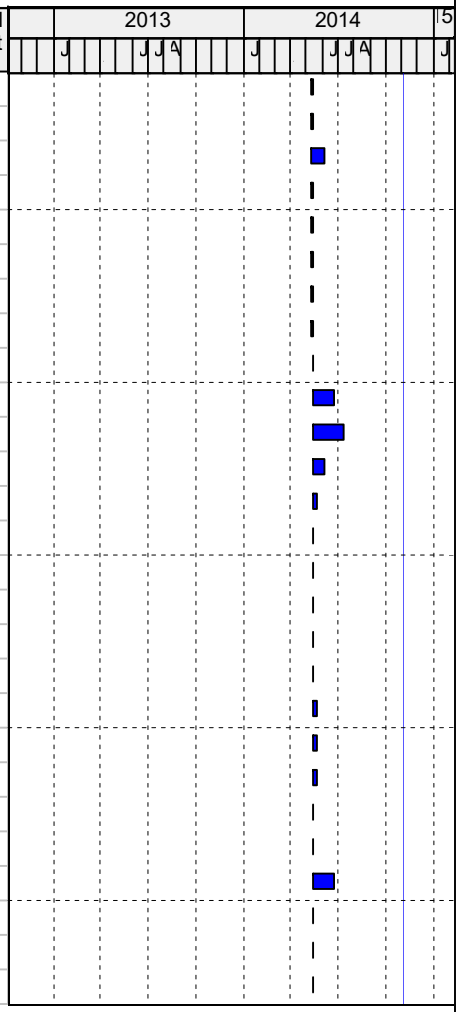



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L12-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L07-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L08-6028 | PreRock at Heat Pumps | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L09-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L10-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L11-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L15-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 19-May-14 A | 19-May-14 A | |
| L07-6028 | PreRock at Heat Pumps | 2 | 0 | 20-May-14 A | 21-May-14 A | |
| L07-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L08-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 20-May-14 A | 21-May-14 A | |
| L10-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L11-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L14-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L07-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 21-May-14 A | 27-May-14 A | |
| L08-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L08-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L09-6028 | PreRock at Heat Pumps | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L10-6014 | Set Tubs & Plumbing RI | 5 | 0 | 21-May-14 A | 27-Jun-14 A | |
| L10-6010 | Frame Walls | 5 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6019 | Complete Top Out GWB | 2 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L11-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L12-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L14-8220 | Plumbing Risers - Install | 2 | 0 | 21-May-14 A | 22-May-14 A | |

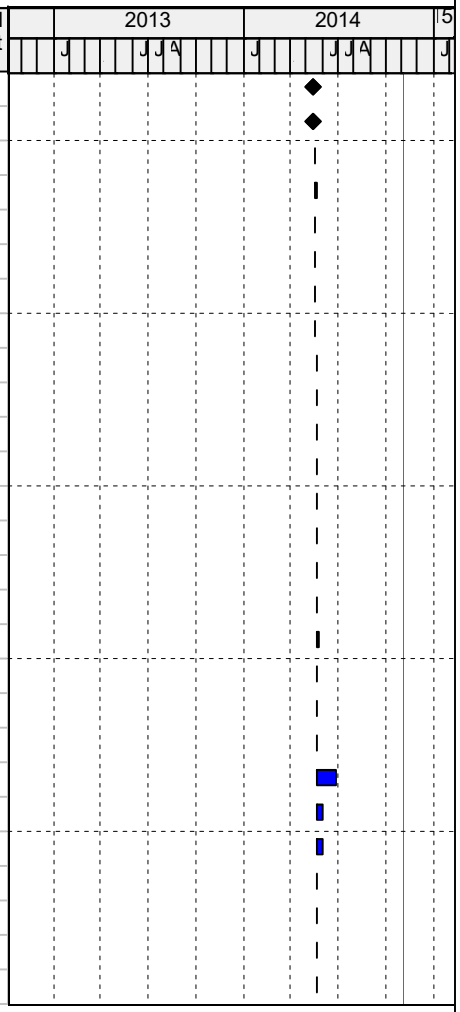



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L16-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L07-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| L08-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 22-May-14 A | 22-May-14 A | |
| L10-6012 | Fire Sprinkler Mains | 5 | 0 | 22-May-14 A | 27-May-14 A | |
| L08-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L09-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6020 | Install Hollow Metal Frames | 3 | 0 | 23-May-14 A | 03-Jun-14 A | |
| L10-6028 | PreRock at Heat Pumps | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L14-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L15-8220 | Plumbing Risers - Install | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L09-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 27-May-14 A | 27-May-14 A | |
| L12-6010 | Frame Walls | 5 | 0 | 27-May-14 A | 02-Jun-14 A | |
| L08-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L09-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 28-May-14 A | 28-May-14 A | |
| L10-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 28-May-14 A | 03-Jun-14 A | |
| L14-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L15-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-May-14 A | 30-May-14 A | |
| L16-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 28-May-14 A | 28-May-14 A | |
| L16-8220 | Plumbing Risers - Install | 2 | 0 | 28-May-14 A | 29-May-14 A | |
| L08-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 29-May-14 A | 30-May-14 A | |
| L10-6016 | Electrical RI | 5 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L10-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| L12-6012 | Fire Sprinkler Mains | 5 | 0 | 30-May-14 A | 26-Jun-14 A | |
| L12-6020 | Install Hollow Metal Frames | 3 | 0 | 30-May-14 A | 02-Jun-14 A | |

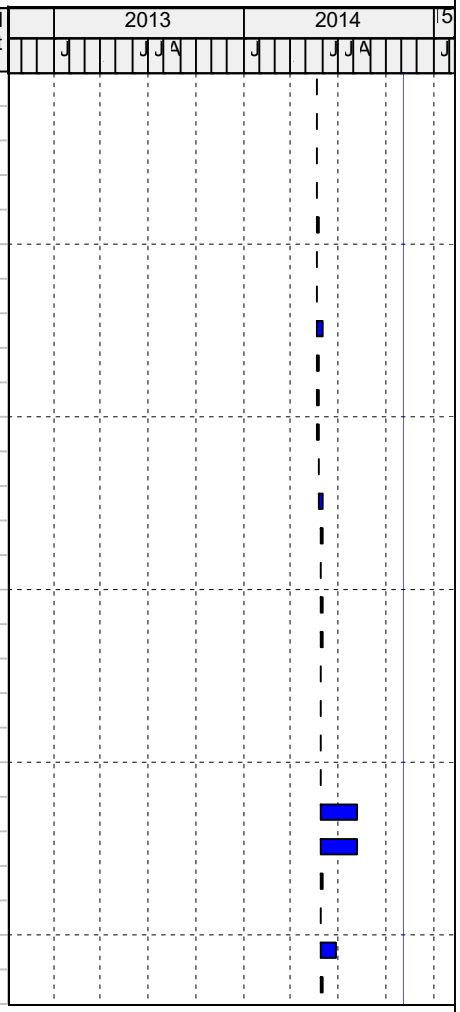


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L17-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L17-8220 | Plumbing Risers - Install | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L10-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L11-6016 | Electrical RI | 5 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L11-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L12-6019 | Complete Top Out GWB | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L14-6020 | Install Hollow Metal Frames | 3 | 0 | 02-Jun-14 A | 05-Jun-14 A | |
| L14-6010 | Frame Walls | 5 | 0 | 02-Jun-14 A | 04-Jun-14 A | |
| L16-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| L14-6019 | Complete Top Out GWB | 2 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L16-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L10-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| L17-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 04-Jun-14 A | 11-Jun-14 A | |
| L08-6016 | Electrical RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L08-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L09-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L12-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L15-6010 | Frame Walls | 3 | 0 | 05-Jun-14 A | 11-Jun-14 A | |
| L09-6012 | Fire Sprinkler Mains | 5 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L09-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L11-6012 | Fire Sprinkler Mains | 4 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L12-6014 | Set Tubs & Plumbing RI | 4 | 0 | 06-Jun-14 A | 27-Jun-14 A | |
| L11-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jun-14 A | 11-Jun-14 A | |
| L09-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-Jun-14 A | 25-Jun-14 A | |
| L14-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L15-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |

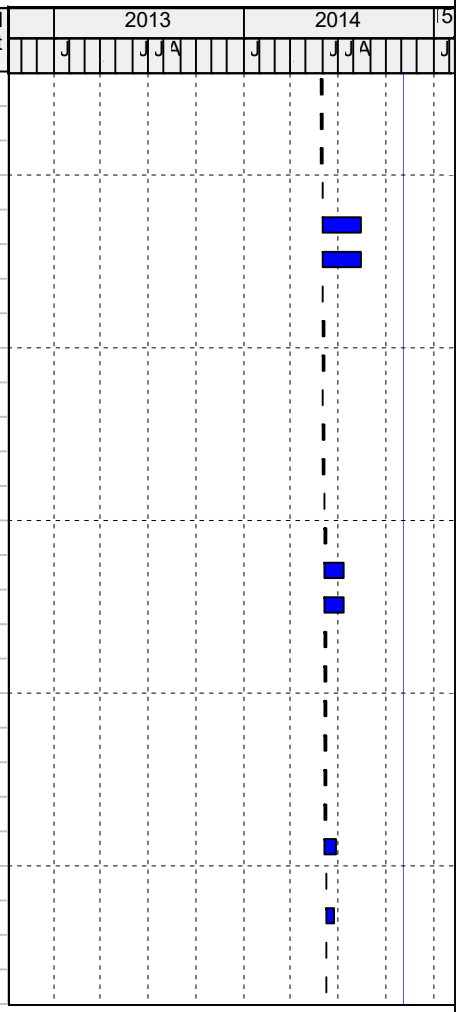


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L09-6016 | Electrical RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L14-6014 | Set Tubs & Plumbing RI | 4 | 0 | 10-Jun-14 A | 21-Jul-14 A | |
| L15-6020 | Install Hollow Metal Frames | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L15-6019 | Complete Top Out GWB | 2 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6014 | Set Tubs & Plumbing RI | 4 | 0 | 11-Jun-14 A | 26-Jun-14 A | |
| L11-6028 | PreRock at Heat Pumps | 2 | 0 | 13-Jun-14 A | 14-Jun-14 A | |
| L11-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 14-Jun-14 A | 14-Jun-14 A | |
| L14-6012 | Fire Sprinkler Mains | 2 | 0 | 16-Jun-14 A | 27-Jun-14 A | |
| L14-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 18-Jun-14 A | 18-Jun-14 A | |
| L15-6023 | Inspection of Exterior Framing | 0 | 0 | 18-Jun-14 A | | |
| L17-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 18-Jun-14 A | 23-Jun-14 A | |
| L17-6010 | Frame Walls | 5 | 0 | 18-Jun-14 A | 29-Jul-14 A | |
| L10-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L12-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6023 | Inspection of Exterior Framing | 0 | 0 | 20-Jun-14 A | | |
| L15-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-Jun-14 A | 20-Jun-14 A | |
| L10-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-Jun-14 A | 23-Jun-14 A | |
| L15-6014 | Set Tubs & Plumbing RI | 5 | 0 | 22-Jun-14 A | 24-Jul-14 A | |
| L08-6018 | HVAC RI | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L12-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |

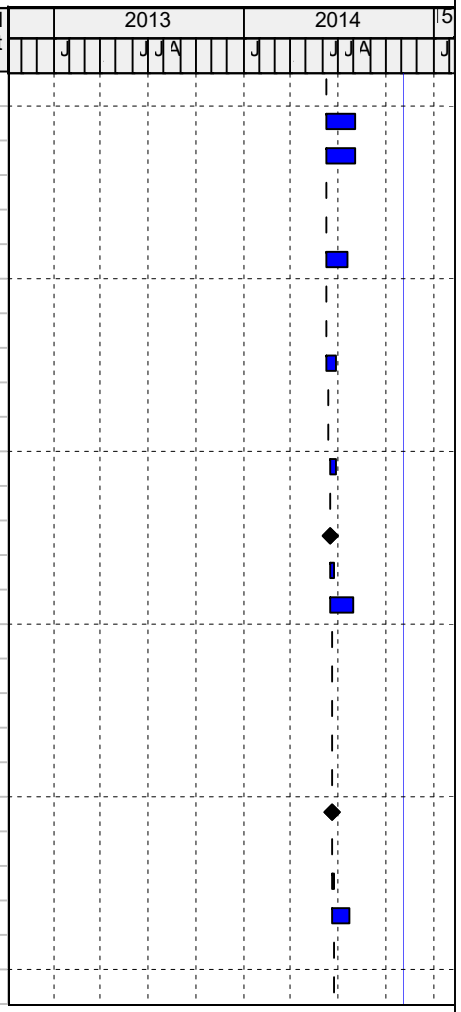


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L15-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L08-6221 | Frame Unit Ceilings | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| L11-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 24-Jun-14 A | 27-Jun-14 A | |
| L12-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L14-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6023 | Inspection of Exterior Framing | 0 | 0 | 24-Jun-14 A | | |
| L12-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| L12-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L14-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L15-6012 | Fire Sprinkler Mains | 2 | 0 | 25-Jun-14 A | 22-Jul-14 A | |
| L16-6023 | Inspection of Exterior Framing | 0 | 0 | 25-Jun-14 A | | |
| L03-6024 | Inspections for GWB Cover | 1 | 0 | 27-Jun-14 A | 27-Jun-14 A | |
| L09-6018 | HVAC RI | 3 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L09-6221 | Frame Unit Ceilings | 2 | 0 | 27-Jun-14 A | 30-Jun-14 A | |
| L12-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L14-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L15-6028 | PreRock at Heat Pumps | 2 | 0 | 30-Jun-14 A | 01-Jul-14 A | |
| L16-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 30-Jun-14 A | 30-Jun-14 A | |
| L16-6010 | Frame Walls | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| L16-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L15-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L15-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L04-6024 | Inspections for GWB Cover | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L10-6018 | HVAC RI | 3 | 0 | 07-Jul-14 A | 21-Jul-14 A | |
| L11-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L15-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |

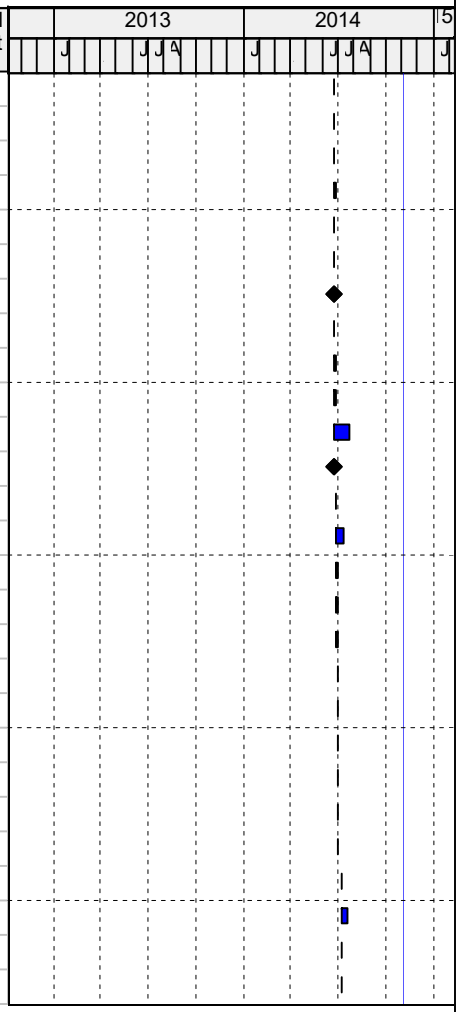



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6012 | Fire Sprinkler Mains | 2 | 0 | 07-Jul-14 A | 24-Jul-14 A | |
| L16-6020 | Install Hollow Metal Frames | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L16-6028 | PreRock at Heat Pumps | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L17-6019 | Complete Top Out GWB | 1 | 0 | 07-Jul-14 A | 08-Aug-14 A | |
| L11-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L15-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 08-Jul-14 A | 04-Aug-14 A | |
| L17-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jul-14 A | 01-Aug-14 A | |
| L10-6221 | Frame Unit Ceilings | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| L17-6012 | Fire Sprinkler Mains | 2 | 0 | 09-Jul-14 A | 12-Aug-14 A | |
| L05-6024 | Inspections for GWB Cover | 2 | 0 | 10-Jul-14 A | 10-Jul-14 A | |
| L04-6000 | Tape/Finish GWB | 6 | 0 | 11-Jul-14 A | 23-Jul-14 A | |
| L16-6019 | Complete Top Out GWB | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L16-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L15-6018 | HVAC RI | 3 | 0 | 16-Jul-14 A | 18-Jul-14 A | |
| L16-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-6024 | Inspections for GWB Cover | 2 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6018 | HVAC RI | 3 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L16-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 21-Jul-14 A | 18-Aug-14 A | |
| L15-6013 | Fire Sprinkler Branch Lines | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| L03-6000 | Tape/Finish GWB | 6 | 0 | 23-Jul-14 A | 29-Jul-14 A | |
| L11-6018 | HVAC RI | 3 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L15-6221 | Frame Unit Ceilings | 2 | 0 | 23-Jul-14 A | 01-Aug-14 A | |
| L16-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L17-6020 | Install Hollow Metal Frames | 3 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| L11-6221 | Frame Unit Ceilings | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |

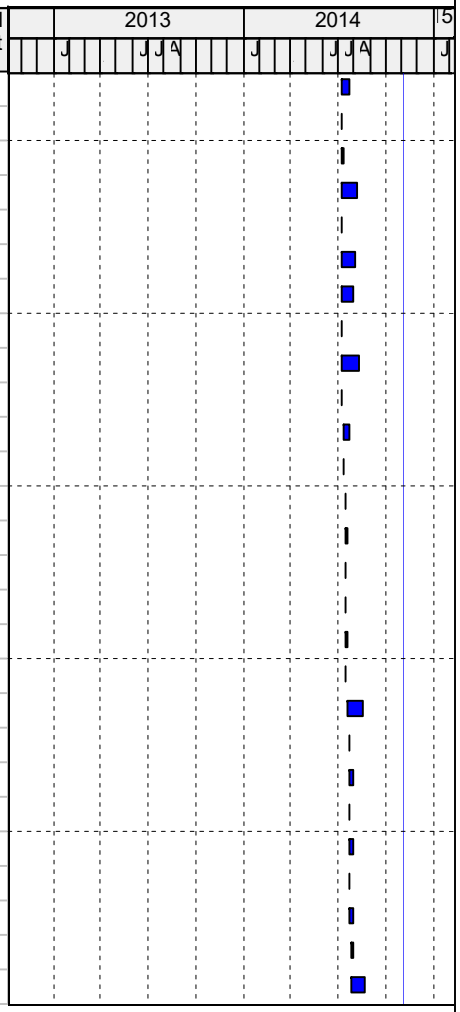


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L14-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L14-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L16-6014 | Set Tubs & Plumbing RI | 5 | 0 | 28-Jul-14 A | 18-Aug-14 A | |
| L07-6024 | Inspections for GWB Cover | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L12-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L05-6000 | Tape/Finish GWB | 6 | 0 | 31-Jul-14 A | 05-Aug-14 A | |
| L08-6024 | Inspections for GWB Cover | 2 | 0 | 31-Jul-14 A | 31-Jul-14 A | |
| L12-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L14-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L06-6000 | Tape/Finish GWB | 4 | 0 | 06-Aug-14 A | 11-Aug-14 A | |
| L09-6024 | Inspections for GWB Cover | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L07-6000 | Tape/Finish GWB | 5 | 0 | 07-Aug-14 A | 16-Aug-14 A | |
| L11-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 08-Aug-14 A | 14-Aug-14 A | |
| L17-6014 | Set Tubs & Plumbing RI | 5 | 0 | 08-Aug-14 A | 16-Sep-14 A | |
| L10-6024 | Inspections for GWB Cover | 2 | 0 | 11-Aug-14 A | 12-Aug-14 A | |
| L09-6000 | Tape/Finish GWB | 5 | 0 | 14-Aug-14 A | 19-Aug-14 A | |
| L08-6000 | Tape/Finish GWB | 5 | 0 | 16-Aug-14 A | 21-Aug-14 A | |
| L11-6024 | Inspections for GWB Cover | 2 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L16-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 18-Aug-14 A | 29-Aug-14 A | |
| L10-6000 | Tape/Finish GWB | 5 | 0 | 19-Aug-14 A | 23-Aug-14 A | |
| L16-6221 | Frame Unit Ceilings | 4 | 0 | 21-Aug-14 A | 26-Aug-14 A | |

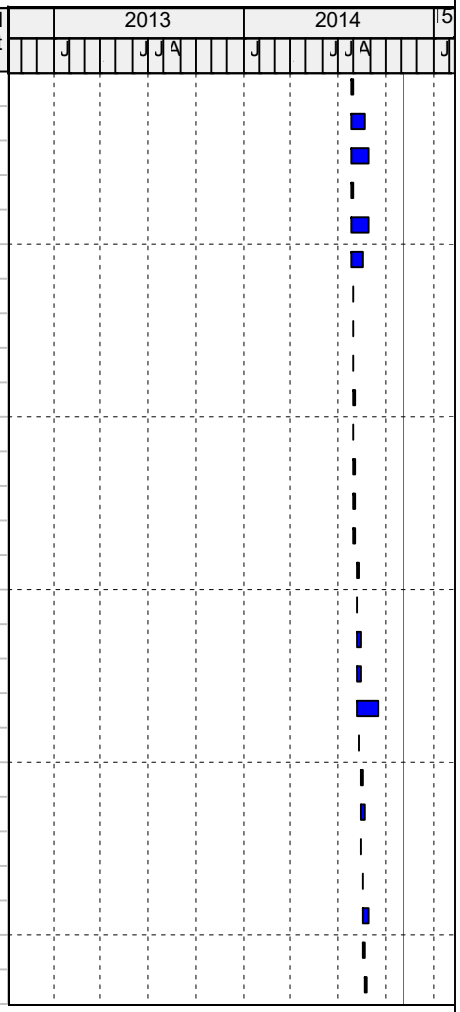



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6018 | HVAC RI | 3 | 0 | 21-Aug-14 A | 10-Sep-14 A | |
| L12-6024 | Inspections for GWB Cover | 2 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L15-6016 | Electrical RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L15-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L11-6000 | Tape/Finish GWB | 5 | 0 | 23-Aug-14 A | 29-Aug-14 A | |
| L17-6221 | Frame Unit Ceilings | 4 | 0 | 26-Aug-14 A | 28-Aug-14 A | |
| L14-6024 | Inspections for GWB Cover | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L16-6016 | Electrical RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L16-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L12-6000 | Tape/Finish GWB | 5 | 0 | 02-Sep-14 A | 08-Sep-14 A | |
| L15-6024 | Inspections for GWB Cover | 2 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L14-6000 | Tape/Finish GWB | 5 | 0 | 06-Sep-14 A | 11-Sep-14 A | |
| L15-6000 | Tape/Finish GWB | 4 | 0 | 12-Sep-14 A | 20-Sep-14 A | |
| L17-6016 | Electrical RI | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-6028 | PreRock at Heat Pumps | 2 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L17-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L17-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L17-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 24-Sep-14 A | 27-Sep-14 A | |
| L17-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L16-6024 | Inspections for GWB Cover | 1 | 0 | 08-Oct-14 A | 09-Oct-14 A | |
| L16-6000 | Tape/Finish GWB | 4 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6024 | Inspections for GWB Cover | 1 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6000 | Tape/Finish GWB | 6 | 4 | 30-Oct-14 A | 07-Nov-14 | 7 |

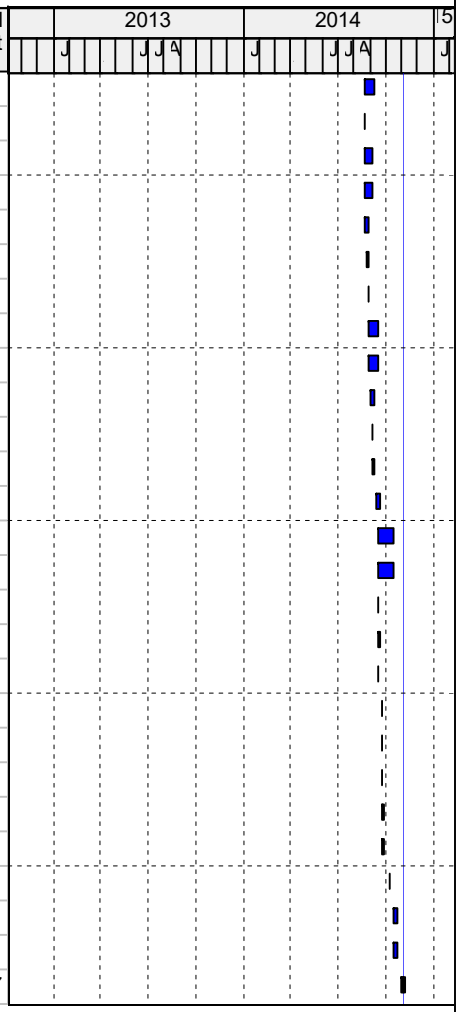



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Mechanical Penthouse** | | | | | | |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 0 | 11-Jun-14 A | 20-Jun-14 A | |
| PH-6006 | PH - Exterior Wall Framing (including PH roof parapet | 6 | 0 | 12-Jun-14 A | 14-Jul-14 A | |
| PH-6014 | PH - Plumbing/Piping RI | 40 | 1 | 25-Jun-14 A | 03-Nov-14 | 0 |
| PH-6002 | PH - Layout | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| PH-6008 | PH - Interior Wall Framing | 3 | 0 | 24-Jul-14 A | 08-Aug-14 A | |
| PH-6020 | PH - H Mtl Frames | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| PH-6012 | PH - Fire Sprinkler RI | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |
| PH-6018 | PH - HVAC RI | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |
| PH-6016 | PH - Electrical RI | 10 | 4 | 23-Sep-14 A | 06-Nov-14 | 43 |
| PH-6022 | PH - Fire Alarm / Elec Specialties RI | 10 | 6 | 23-Sep-14 A | 10-Nov-14 | 41 |
| **Finishes** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL4-8100 | LL4 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| LL4-8102 | LL4 - GWB Hang (incl. screw inspection) | 3 | 1 | 27-Oct-14 A | 03-Nov-14 | 31 |
| LL4-8104 | LL4 - Int Painting | 1 | 1 | 07-Nov-14 | 07-Nov-14 | 31 |
| LL4-8122 | LL4 - Plumbing Trim / Finish | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 37 |
| LL4-8108 | LL4 - Elec Trim / Finish | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 37 |
| LL4-8110 | LL4 - HVAC Trim / Finish | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 37 |
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 31 |
| LL4-8118 | LL4 - Elec Specialties Trim / Finish | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 31 |
| LL4-8124 | LL4 - Flooring (VCT) | 3 | 3 | 14-Nov-14 | 18-Nov-14 | 37 |
| LL4-8126 | LL4 - Doors & Hardware | 2 | 2 | 19-Nov-14 | 20-Nov-14 | 37 |
| LL4-8114 | LL4 - Striping / Signage | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 37 |
| LL4-8132 | LL4 - Punch | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 37 |

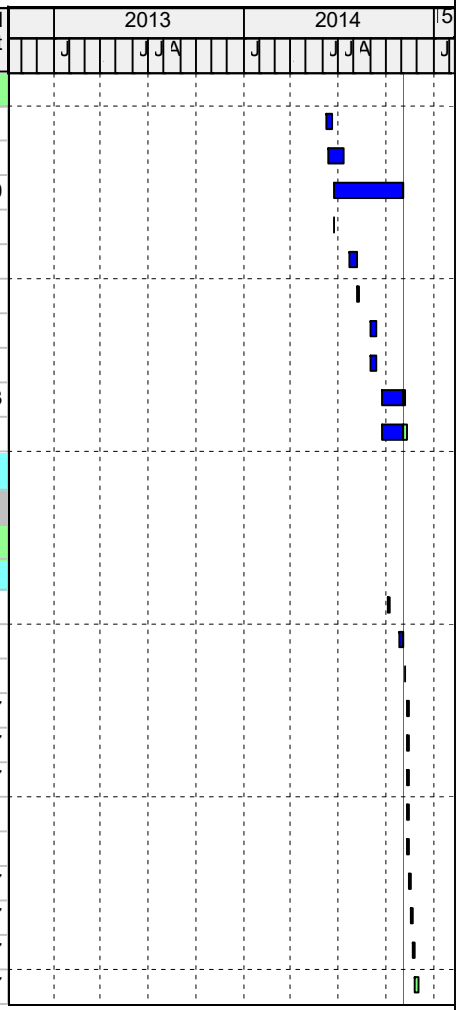



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8134 | LL4 - Clean | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 37 |
| LL4-8214 | LL4 - Floor Complete | 0 | 0 | | 02-Dec-14 | 37 |
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL3-8100 | LL3 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| LL3-8102 | LL3 - GWB Hang (incl. screw inspection) | 3 | 1 | 27-Oct-14 A | 03-Nov-14 | 31 |
| LL3-8104 | LL3 - Int Painting | 1 | 1 | 07-Nov-14 | 07-Nov-14 | 31 |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 37 |
| LL3-8108 | LL3 - Elec Trim / Finish | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 37 |
| LL3-8110 | LL3 - HVAC Trim / Finish | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 37 |
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 31 |
| LL3-8118 | LL3 - Elec Specialties Trim / Finish | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 31 |
| LL3-8124 | LL3 - Flooring (VCT) | 3 | 3 | 14-Nov-14 | 18-Nov-14 | 37 |
| LL3-8126 | LL3 - Doors & Hardware | 2 | 2 | 19-Nov-14 | 20-Nov-14 | 37 |
| LL3-8114 | LL3 - Striping / Signage | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 37 |
| LL3-8132 | LL3 - Punch | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 37 |
| LL3-8134 | LL3 - Clean | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 37 |
| LL3-8214 | LL3 - Floor Complete | 0 | 0 | | 02-Dec-14 | 37 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL2E-8102 | LL2 - GWB Hang / Tape / Finish @ Electrical Rooms | 8 | 0 | 24-Jun-14 A | 03-Jul-14 A | |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish & Inspection | 6 | 2 | 16-Sep-14 A | 04-Nov-14 | 37 |
| LL2-8100 | LL2 - Insulation | 5 | 0 | 16-Sep-14 A | 09-Oct-14 A | |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 5 | 0 | 17-Sep-14 A | 27-Oct-14 A | |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| LL2-8136 | LL2 - Chainlink Fencing / Gate @ Recycling | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 38 |
| LL2-8104 | LL2 - Int Painting | 5 | 5 | 05-Nov-14 | 11-Nov-14 | 31 |

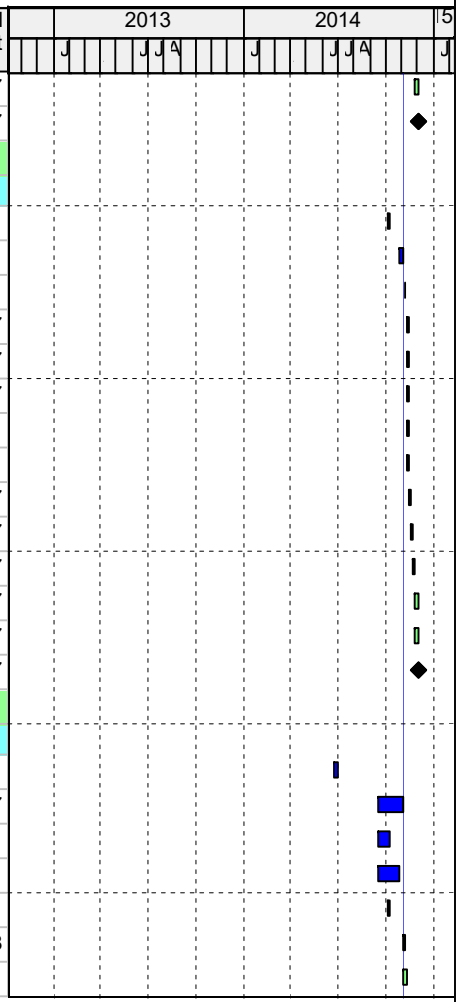



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-8128 | LL2 - Entry Gates | 3 | 3 | 07-Nov-14 | 11-Nov-14 | 37 |
| LL2-8122 | LL2 - Plumbing Trim / Finish | 3 | 3 | 10-Nov-14 | 12-Nov-14 | 44 |
| LL2-8108 | LL2 - Elec Trim / Finish | 4 | 4 | 10-Nov-14 | 13-Nov-14 | 53 |
| LL2-8110 | LL2 - HVAC Trim / Finish | 3 | 3 | 10-Nov-14 | 12-Nov-14 | 54 |
| LL2-8112 | LL2 - Fire Sprinkler Trim / Finish | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 33 |
| LL2-8118 | LL2 - Elec Specialties Trim / Finish | 4 | 4 | 10-Nov-14 | 13-Nov-14 | 31 |
| LL2-8116 | LL2 - Finish Carpentry / Millwork | 3 | 3 | 11-Nov-14 | 13-Nov-14 | 43 |
| LL2-8124 | LL2 - Flooring | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 35 |
| LL2-8120 | LL2 - Install Bollards | 3 | 3 | 12-Nov-14 | 14-Nov-14 | 37 |
| LL2-8114 | LL2 - Striping / Signage | 5 | 5 | 19-Nov-14 | 25-Nov-14 | 35 |
| LL2-8126 | LL2 - Doors & Hardware | 4 | 4 | 19-Nov-14 | 24-Nov-14 | 36 |
| LL2-8132 | LL2 - Punch | 5 | 5 | 26-Nov-14 | 04-Dec-14 | 35 |
| LL2-8134 | LL2 - Clean | 5 | 5 | 26-Nov-14 | 04-Dec-14 | 35 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 31-Jul-14 A | |
| LL1-Z2U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 09-May-14 A | |
| LL1-Z3U-8102 | Above Ceiling GWB (At All Areas North of Q-Line) | 5 | 0 | 10-Feb-14 A | 20-Jun-14 A | |
| L1BU-8102 | Above Ceiling GWB [including East Service Corridor] | 5 | 0 | 06-Jun-14 A | 11-Jun-14 A | |
| L1LU-8102 | Above Ceiling GWB | 5 | 0 | 24-Jun-14 A | 13-Oct-14 A | |
| L1KU-8102 | Above Ceiling GWB | 2 | 0 | 26-Jun-14 A | 22-Aug-14 A | |
| LL1-8100 | Insulation | 5 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| LL1-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 28-Jul-14 A | 06-Aug-14 A | |
| LL1-Z2-8102 | GWB Hang (Walls) & Inspection | 4 | 0 | 11-Aug-14 A | 14-Aug-14 A | |
| LL1-Z2-8100 | Insulation | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| LL1-8215 | GWB Tape (Walls) | 10 | 2 | 16-Aug-14 A | 04-Nov-14 | 3 |
| LL1-Z3-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 15-Sep-14 A | 07-Oct-14 A | |

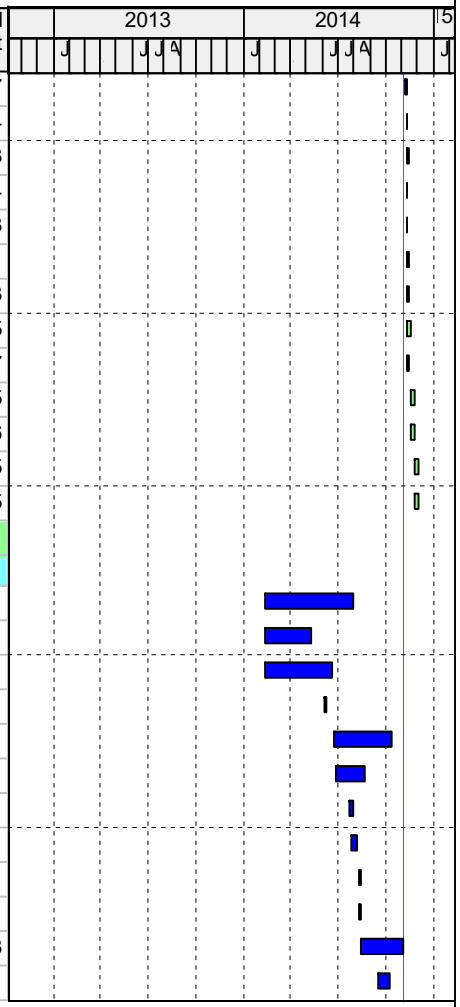


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8100 | Insulation | 5 | 0 | 15-Sep-14 A | 24-Sep-14 A | |
| LL1-Z2-8215 | GWB Tape (Walls/Ceilings) | 7 | 1 | 29-Sep-14 A | 05-Nov-14 | 12 |
| L1B-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L1K-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| LL1-Z3-8215 | GWB Tape (Walls & Ceilings) | 7 | 2 | 07-Oct-14 A | 04-Nov-14 | 11 |
| L1K-8102 | GWB Hang (Walls) & Inspection | 8 | 0 | 09-Oct-14 A | 31-Oct-14 A | |
| L1L-8100 | Insulation | 4 | 0 | 13-Oct-14 A | 16-Oct-14 A | |
| L1B-8102 | GWB Hang (Walls) & Inspection - Main Ballroom N/S/ | 4 | 0 | 16-Oct-14 A | 22-Oct-14 A | |
| L1L-8102 | GWB Hang (Walls) | 4 | 3 | 30-Oct-14 A | 05-Nov-14 | 1 |
| L1K-8215 | GWB Tape (Walls & Ceilings) | 4 | 4 | 03-Nov-14 | 06-Nov-14 | 9 |
| LL1-8104 | Prime Paint | 5 | 5 | 05-Nov-14 | 11-Nov-14 | 8 |
| LL1-Z3-8104 | Prime Paint | 4 | 4 | 05-Nov-14 | 10-Nov-14 | 11 |
| LL1-Z2-8104 | Prime Paint | 2 | 2 | 06-Nov-14 | 07-Nov-14 | 12 |
| L1L-8215 | GWB Tape (Walls) | 7 | 7 | 06-Nov-14 | 14-Nov-14 | 1 |
| L1K-8104 | Prime Paint | 4 | 4 | 07-Nov-14 | 12-Nov-14 | 9 |
| LL1-Z2-8114 | T Bar Grid Ceiling & Inspection | 3 | 3 | 10-Nov-14 | 12-Nov-14 | 12 |
| LL1-8114 | T Bar Grid Ceiling & Inspection | 4 | 4 | 11-Nov-14 | 14-Nov-14 | 8 |
| LL1-Z3-8114 | T Bar Grid Ceiling & Inspection | 4 | 4 | 11-Nov-14 | 14-Nov-14 | 11 |
| L1K-8106 | Wallcoverings (FRP) | 1 | 1 | 13-Nov-14 | 13-Nov-14 | 9 |
| L1K-8114 | T Bar Grid Ceiling | 4 | 4 | 13-Nov-14 | 18-Nov-14 | 15 |
| LL1-Z2-8124 | Flooring | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 12 |
| LL1-Z2-8106 | Wallcoverings | 2 | 2 | 19-Nov-14 | 20-Nov-14 | 23 |
| LL1-Z3-8124 | Flooring (Epoxy) | 5 | 5 | 22-Nov-14 | 26-Nov-14 | 19 |
| LL1-Z2-8116 | Finish Carpentry / Millwork | 5 | 5 | 25-Nov-14 | 03-Dec-14 | 12 |
| L1B-8215 | GWB Tape (Walls & Ceilings) | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 9 |
| L1K-8140 | Acoustical Ceiling Tile | 4 | 4 | 25-Nov-14 | 02-Dec-14 | 9 |
| LL1-Z3-8116 | Finish Carpentry / Millwork | 4 | 4 | 26-Nov-14 | 03-Dec-14 | 11 |

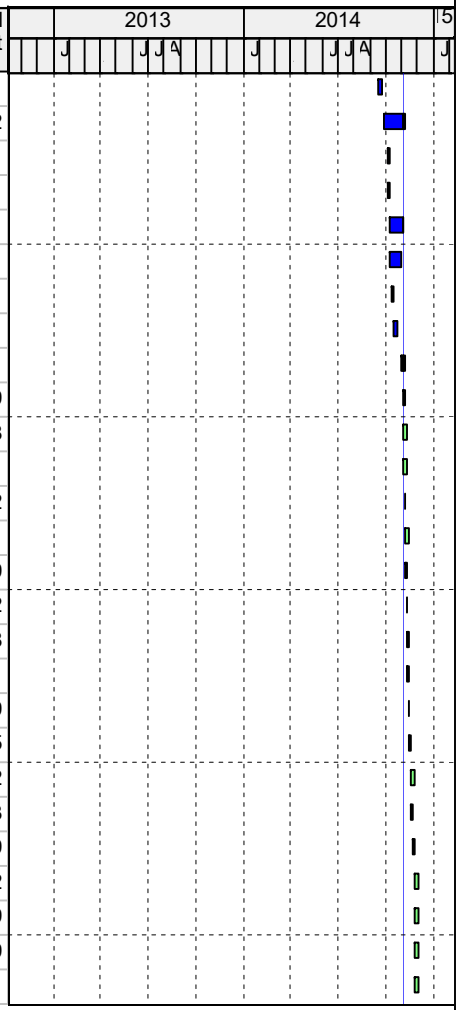



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 9 |
| L1K-8124 | Flooring (VCT & Tile) | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 9 |
| L1K-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 9 |
| LL1-8124 | Flooring | 3 | 3 | 02-Dec-14 | 04-Dec-14 | 3 |
| LL1-Z3-8126 | Doors & Hardware | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 11 |
| L1B-8104 | Prime Paint | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 9 |
| LL1-Z2-8126 | Doors & Hardware | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 12 |
| L1B-8114 | T Bar Grid Ceiling | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 9 |
| LL1-8116 | Finish Carpentry / Millwork | 5 | 5 | 08-Dec-14 | 12-Dec-14 | 3 |
| LL1-Z2-8140 | Acoustical Ceiling Tile | 2 | 2 | 09-Dec-14 | 10-Dec-14 | 12 |
| LL1-Z3-8140 | Acoustical Ceiling Tile | 3 | 3 | 09-Dec-14 | 11-Dec-14 | 11 |
| LL1-Z2-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 10-Dec-14 | 12-Dec-14 | 12 |
| LL1-Z2-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 10-Dec-14 | 12-Dec-14 | 12 |
| LL1-8126 | Doors & Hardware | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 3 |
| LL1-Z3-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 11 |
| LL1-Z3-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 11 |
| L1K-8116 | Finish Carpentry / Millwork | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 9 |
| L1K-8126 | Doors & Hardware | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 9 |
| L1B-8124 | Flooring (Carpet) | 4 | 4 | 12-Dec-14 | 17-Dec-14 | 9 |
| LL1-8140 | Acoustical Ceiling Tile | 3 | 3 | 16-Dec-14 | 18-Dec-14 | 3 |
| L1L-8104 | Prime Paint | 3 | 3 | 16-Dec-14 | 18-Dec-14 | 1 |
| LL1-Z2-8132 | Punch | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 22 |
| LL1-Z2-8134 | Clean | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 22 |
| L1B-8116 | Finish Carpentry / Millwork | 4 | 4 | 18-Dec-14 | 23-Dec-14 | 13 |
| L1B-8126 | Doors & Hardware | 4 | 4 | 18-Dec-14 | 23-Dec-14 | 13 |
| L1B-8140 | Acoustical Ceiling Tile | 4 | 4 | 18-Dec-14 | 23-Dec-14 | 9 |
| LL1-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 19-Dec-14 | 23-Dec-14 | 3 |

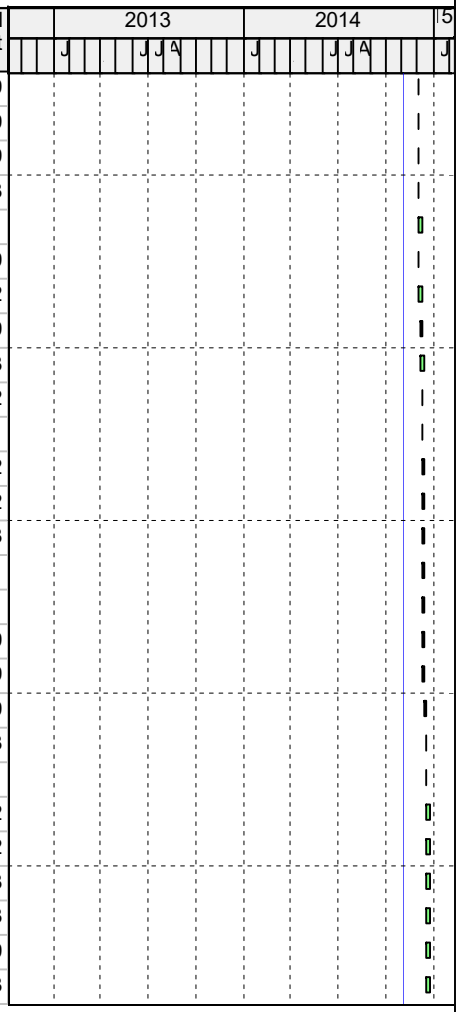



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8114 | Install wood ceiling supports | 2 | 2 | 19-Dec-14 | 22-Dec-14 | 1 |
| LL1-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 22-Dec-14 | 24-Dec-14 | 3 |
| LL1-Z3-8132 | Punch | 4 | 4 | 23-Dec-14 | 30-Dec-14 | 19 |
| LL1-Z3-8134 | Clean | 4 | 4 | 23-Dec-14 | 30-Dec-14 | 19 |
| L1B-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 23-Dec-14 | 30-Dec-14 | 9 |
| L1B-8118 | Elec & Specialties Trim / Finish | 4 | 4 | 23-Dec-14 | 30-Dec-14 | 9 |
| L1L-8106 | Wallcoverings | 5 | 5 | 23-Dec-14 | 31-Dec-14 | 1 |
| LL1-8132 | Punch | 4 | 4 | 02-Jan-15 | 07-Jan-15 | 14 |
| LL1-8134 | Clean | 4 | 4 | 02-Jan-15 | 07-Jan-15 | 14 |
| L1L-8124 | Flooring | 5 | 5 | 02-Jan-15 | 08-Jan-15 | 1 |
| L1L-8140 | Install wood ceiling | 6 | 6 | 07-Jan-15 | 14-Jan-15 | 1 |
| L1B-8132 | Punch | 4 | 4 | 08-Jan-15 | 13-Jan-15 | 10 |
| L1B-8134 | Clean | 4 | 4 | 08-Jan-15 | 13-Jan-15 | 10 |
| L1K-8132 | Punch | 5 | 5 | 08-Jan-15 | 14-Jan-15 | 9 |
| L1K-8134 | Clean | 5 | 5 | 08-Jan-15 | 14-Jan-15 | 9 |
| L1L-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 09-Jan-15 | 12-Jan-15 | 1 |
| L1L-8116 | Finish Carpentry / Millwork | 4 | 4 | 09-Jan-15 | 14-Jan-15 | 1 |
| L1L-8126 | Doors & Hardware | 4 | 4 | 09-Jan-15 | 14-Jan-15 | 1 |
| L1L-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 09-Jan-15 | 12-Jan-15 | 1 |
| L1L-8132 | Punch | 4 | 4 | 21-Jan-15 | 26-Jan-15 | 1 |
| L1L-8134 | Clean | 4 | 4 | 21-Jan-15 | 26-Jan-15 | 1 |
| **Corridors / Common / Public Areas** | | | | | | |
| LL1-Z2-8200 | First Coat Finish Paint | 3 | 3 | 14-Nov-14 | 18-Nov-14 | 12 |
| LL1-8200 | First Coat Finish Paint | 4 | 4 | 18-Nov-14 | 21-Nov-14 | 8 |
| LL1-Z3-8200 | First Coat Finish Paint | 4 | 4 | 18-Nov-14 | 21-Nov-14 | 11 |
| L1K-8200 | First Coat Finish Paint | 5 | 5 | 19-Nov-14 | 25-Nov-14 | 9 |
| L1K-8204 | HVAC Trim / Finish | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 9 |





© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-8200 | First Coat Finish Paint | 3 | 3 | 09-Dec-14 | 11-Dec-14 | 9 |
| LL1-Z2-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 10-Dec-14 | 12-Dec-14 | 12 |
| LL1-Z3-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 11 |
| LL1-Z2-8201 | Final Coat Finish Paint | 3 | 3 | 12-Dec-14 | 16-Dec-14 | 22 |
| LL1-Z3-8201 | Final Coat Finish Paint | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 19 |
| L1K-8201 | Final Coat Finish Paint | 4 | 4 | 16-Dec-14 | 19-Dec-14 | 9 |
| LL1-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 23-Dec-14 | 29-Dec-14 | 3 |
| L1B-8204 | Mech Trim / Finish (HVAC & Plumbing) | 4 | 4 | 23-Dec-14 | 30-Dec-14 | 9 |
| L1L-8200 | First Coat Finish Paint | 5 | 5 | 23-Dec-14 | 31-Dec-14 | 1 |
| LL1-Z2-8214 | LL1 Zone 2 Compllete | 0 | 0 | | 23-Dec-14 | 22 |
| LL1-8201 | Final Coat Finish Paint | 4 | 4 | 24-Dec-14 | 31-Dec-14 | 14 |
| LL1-Z3-8214 | LL1, Zone 3 Complete | 0 | 0 | | 30-Dec-14 | 19 |
| L1B-8201 | Final Coat Finish Paint | 5 | 5 | 31-Dec-14 | 07-Jan-15 | 10 |
| LL1-8214 | LL1, Zone 1 Complete | 0 | 0 | | 07-Jan-15 | 14 |
| L1L-8204 | Mech Trim / Finish (HVAC & Plumbing) | 2 | 2 | 09-Jan-15 | 12-Jan-15 | 1 |
| L1B-8214 | L1, Zone 2 Complete | 0 | 0 | | 13-Jan-15 | 10 |
| L1L-8201 | Final Coat Finish Paint | 5 | 5 | 14-Jan-15 | 20-Jan-15 | 1 |
| L1K-8214 | L1, Zone 1 Complete | 0 | 0 | | 14-Jan-15 | 9 |
| L1L-8214 | L1, Zone 4 Complete | 0 | 0 | | 26-Jan-15 | 1 |
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8100 | L2 - Insulation - North Half | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L02-8102 | L2 - GWB Hang / Tape / Finish - North Half | 7 | 5 | 23-Oct-14 A | 07-Nov-14 | 19 |
| L02-8104 | L2 - Int Painting - North Half | 3 | 3 | 08-Nov-14 | 11-Nov-14 | 19 |
| L02-8106 | L2 - Wallcoverings | 4 | 4 | 12-Nov-14 | 17-Nov-14 | 16 |
| L02-8124 | L2 - Flooring | 5 | 5 | 18-Nov-14 | 24-Nov-14 | 16 |
| L02-8108 | L2 - Elec Trim / Finish | 5 | 5 | 19-Nov-14 | 25-Nov-14 | 22 |

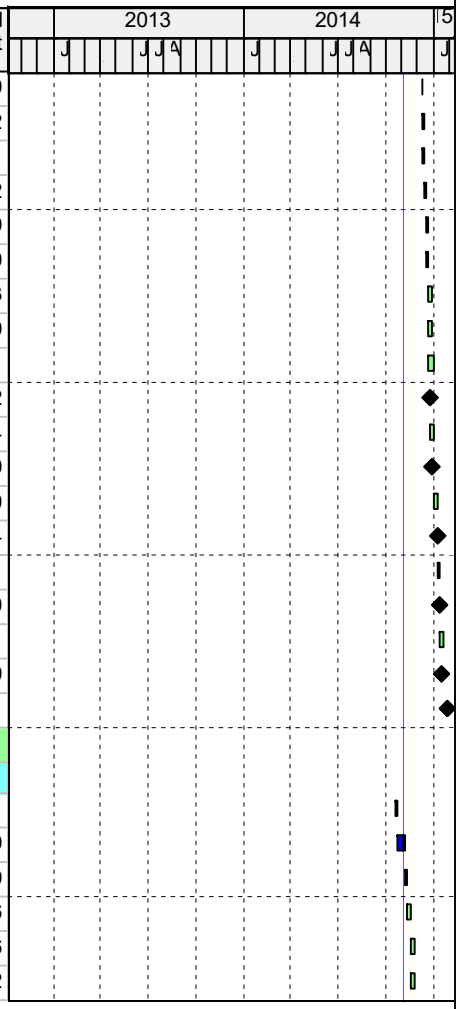


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8110 | L2 - HVAC Trim / Finish | 5 | 5 | 19-Nov-14 | 25-Nov-14 | 22 |
| L02-8112 | L2 - Fire Sprinkler Trim / Finish | 5 | 5 | 19-Nov-14 | 25-Nov-14 | 22 |
| L02-8118 | L2 - Elec Specialties Trim / Finish | 5 | 5 | 19-Nov-14 | 25-Nov-14 | 22 |
| L02-8116 | L2 - Finish Carpentry / Millwork | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 16 |
| L02-8120 | L2 - Ceramic Tile / Counter Tops | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 16 |
| L02-8128 | L2 - Bath Specialties | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 22 |
| L02-8122 | L2 - Plumbing Trim / Finish | 5 | 5 | 26-Nov-14 | 04-Dec-14 | 24 |
| L02-8126 | L2 - Doors & Hardware | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 17 |
| L02-8136 | L2 - Lockers / Benches @ Locker Rooms | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 16 |
| L02-8132 | L2 - Punch | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 16 |
| L02-8134 | L2 - Clean | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 16 |
| **Corridors** | | | | | | |
| L02-8200 | L2 - Final Paint @ Common / Public Areas | 5 | 5 | 10-Dec-14 | 16-Dec-14 | 16 |
| L02-8114 | L2 - Signage | 3 | 3 | 17-Dec-14 | 19-Dec-14 | 24 |
| L02-8210 | L2 - Owner Walk / Create Punchlist | 1 | 1 | 24-Dec-14 | 24-Dec-14 | 16 |
| L02-8212 | L2 - Resolve Final Punchlist | 5 | 5 | 29-Dec-14 | 05-Jan-15 | 16 |
| L02-8214 | Floor Complete | 0 | 0 | | 05-Jan-15 | 16 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L03-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L04-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L05-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L06-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L07-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L08-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L09-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |

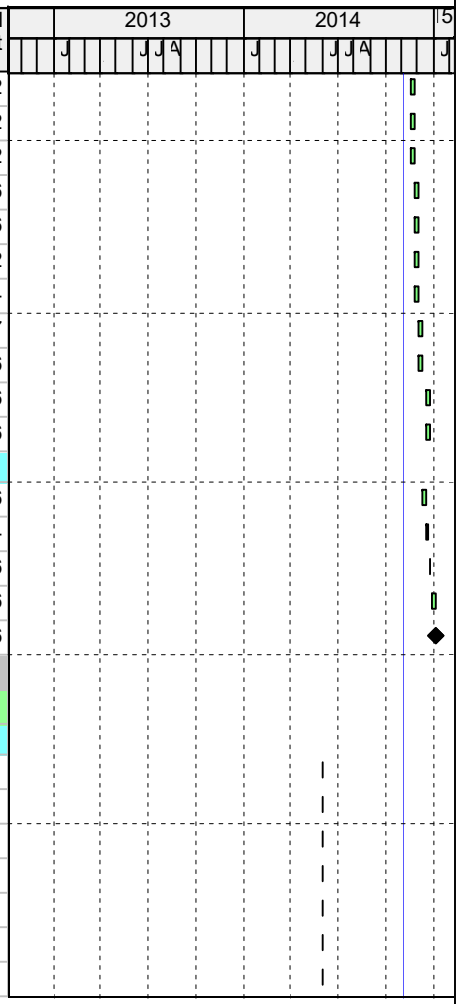



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L11-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L12-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L14-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L15-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L16-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L17-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L03-8102S | Stock GWB | 2 | 0 | 27-Jun-14 A | 08-Jul-14 A | |
| L04-8102 | Hang GWB & Inspection | 4 | 0 | 07-Jul-14 A | 16-Jul-14 A | |
| L04-8102S | Stock GWB | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-8102 | Hang GWB & Inspection | 5 | 0 | 09-Jul-14 A | 22-Jul-14 A | |
| L05-8102S | Stock GWB | 2 | 0 | 10-Jul-14 A | 14-Jul-14 A | |
| L05-8102 | Hang GWB & Inspection | 4 | 0 | 17-Jul-14 A | 23-Jul-14 A | |
| L06-8102S | Stock GWB | 2 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L04-8104 | Paint (Prime) | 2 | 0 | 28-Jul-14 A | 05-Aug-14 A | |
| L03-8104 | Paint (Prime) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L03-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L07-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L08-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L06-8102 | Hang GWB & Inspection | 5 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L07-8102 | Hang GWB & Inspection | 6 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L04-8105 | Paint (First Coat & Ceilings) | 5 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L05-8104 | Paint (Prime) | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| L09-8102S | Stock GWB | 2 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 07-Aug-14 A | 11-Aug-14 A | |
| L09-8102 | Hang GWB & Inspection | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| L08-8102 | Hang GWB & Inspection | 6 | 0 | 11-Aug-14 A | 15-Aug-14 A | |

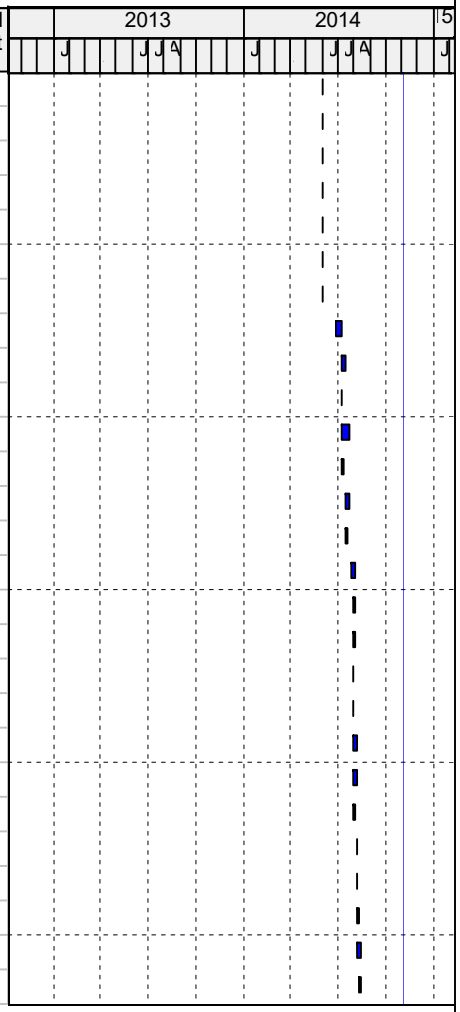



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8104 | Paint (Prime) | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L10-8102S | Stock GWB | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-8102 | Hang GWB & Inspection | 4 | 0 | 13-Aug-14 A | 18-Aug-14 A | |
| L06-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 14-Aug-14 A | 18-Aug-14 A | |
| L11-8102S | Stock GWB | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L07-8104 | Paint (Prime) | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L11-8102 | Hang GWB & Inspection | 4 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| L07-8105 | Paint (First Coat & Ceilings) | 4 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L09-8104 | Paint (Prime) | 2 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L08-8104 | Paint (Prime) | 2 | 0 | 22-Aug-14 A | 25-Aug-14 A | |
| L12-8102 | Hang GWB & Inspection | 4 | 0 | 22-Aug-14 A | 30-Aug-14 A | |
| L12-8102S | Stock GWB | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8108 | Elec Trim / Finish | 4 | 0 | 25-Aug-14 A | 04-Sep-14 A | |
| L08-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L03-8118 | Fire Alarm Trim / Finish | 3 | 0 | 27-Aug-14 A | 29-Sep-14 A | |
| L14-8102S | Stock GWB | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L09-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 29-Aug-14 A | 09-Sep-14 A | |
| L14-8102 | Hang GWB & Inspection | 5 | 0 | 29-Aug-14 A | 05-Sep-14 A | |
| L03-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 02-Sep-14 A | 05-Sep-14 A | |
| L04-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 04-Sep-14 A | 09-Sep-14 A | |
| L10-8104 | Paint (Prime) | 2 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| L15-8102S | Stock GWB | 1 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L15-8102 | Hang GWB & Inspection | 5 | 0 | 06-Sep-14 A | 12-Sep-14 A | |
| L03-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8108 | Elec Trim / Finish | 4 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L04-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 11-Sep-14 A | |
| L05-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 08-Sep-14 A | 12-Sep-14 A | |

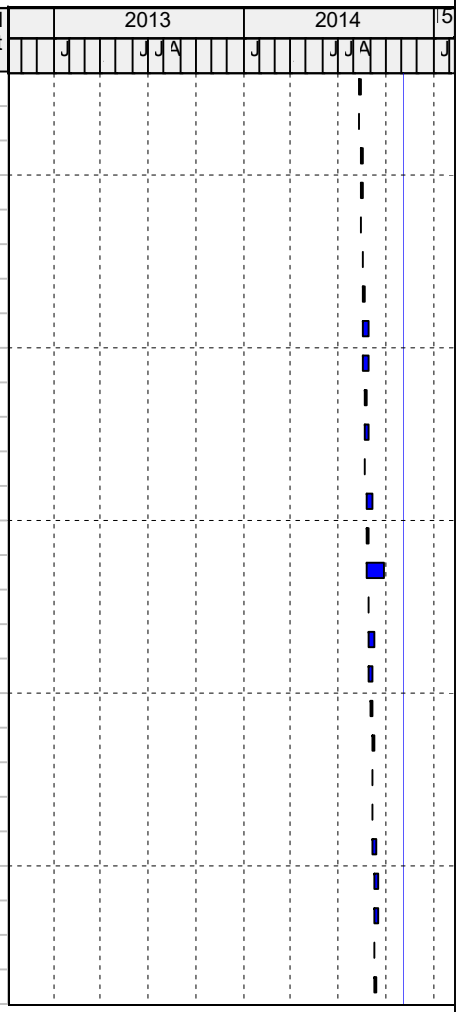



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 08-Sep-14 A | 12-Sep-14 A | |
| L11-8104 | Paint (Prime) | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L04-8116 | Install Base at Guestrooms | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L11-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 10-Sep-14 A | 22-Sep-14 A | |
| L03-8116 | Install Base at Guestrooms | 5 | 0 | 12-Sep-14 A | 16-Sep-14 A | |
| L12-8104 | Paint (Prime) | 2 | 0 | 12-Sep-14 A | 17-Sep-14 A | |
| L05-8116 | Install Base at Guestrooms | 5 | 0 | 16-Sep-14 A | 24-Sep-14 A | |
| L06-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L05-8108 | Elec Trim / Finish | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L07-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 17-Sep-14 A | 23-Sep-14 A | |
| L12-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 17-Sep-14 A | 06-Oct-14 A | |
| L06-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L07-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L14-8104 | Paint (Prime) | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L06-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L06-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L08-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L14-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 24-Sep-14 A | 06-Oct-14 A | |
| L15-8104 | Paint (Prime) | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L03-8110 | HVAC Grilles & Registers | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L03-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8118 | Fire Alarm Trim / Finish | 3 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L10-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 29-Sep-14 A | 01-Oct-14 A | |

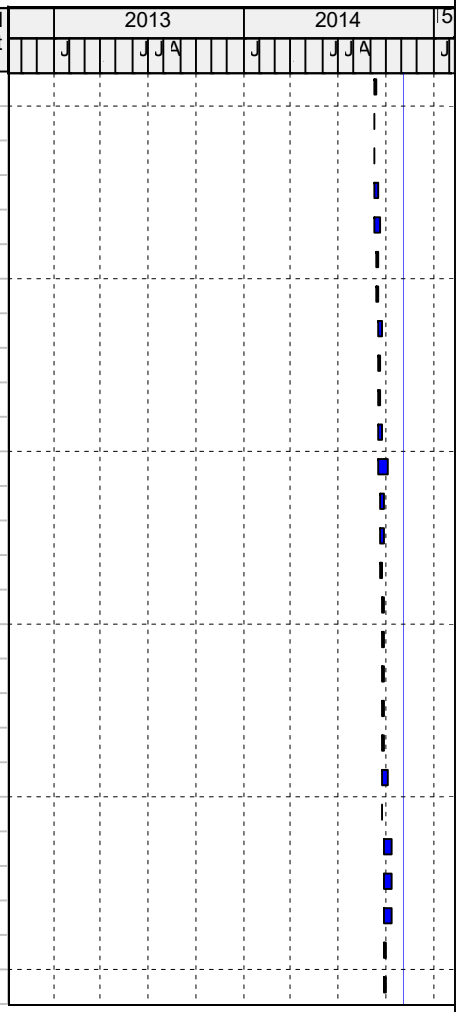



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 30-Sep-14 A | 06-Oct-14 A | |
| L03-8126 | Install Doors | 3 | 0 | 01-Oct-14 A | 07-Oct-14 A | |
| L03-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 01-Oct-14 A | 28-Oct-14 A | |
| L04-8126 | Install Doors | 3 | 0 | 02-Oct-14 A | 09-Oct-14 A | |
| L08-8116 | Install Base at Guestrooms | 5 | 0 | 02-Oct-14 A | 08-Oct-14 A | |
| L04-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8118 | Fire Alarm Trim / Finish | 3 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8108 | Elec Trim / Finish | 4 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L15-8105 | Paint - First Coast & Ceilings | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8126 | Install Doors | 3 | 0 | 08-Oct-14 A | 10-Oct-14 A | |
| L09-8116 | Install Base and Door Thresholds | 5 | 0 | 08-Oct-14 A | 15-Oct-14 A | |
| L09-8124 | Install Flooring | 5 | 0 | 08-Oct-14 A | 14-Oct-14 A | |
| L16-8102S | Stock GWB | 1 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L09-8112 | Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 10-Oct-14 A | |
| L16-8102 | Hang GWB & Inspection | 4 | 0 | 10-Oct-14 A | 17-Oct-14 A | |
| L06-8118 | Fire Alarm Trim / Finish | 3 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L09-8108 | Lighting and Electrical Trim | 3 | 0 | 13-Oct-14 A | 15-Oct-14 A | |
| L10-8124 | Install Flooring | 5 | 0 | 13-Oct-14 A | 16-Oct-14 A | |
| L11-8112 | Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L03-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 2 | 14-Oct-14 A | 04-Nov-14 | 40 |
| L06-8110 | HVAC Grilles & Registers | 2 | 0 | 14-Oct-14 A | 21-Oct-14 A | |
| L06-8126 | Install Doors | 2 | 0 | 14-Oct-14 A | 20-Oct-14 A | |
| L07-8118 | Fire Alarm Trim / Finish | 3 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L12-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L14-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L08-8118 | Fire Alarm Trim / Finish | 3 | 0 | 15-Oct-14 A | 16-Oct-14 A | |

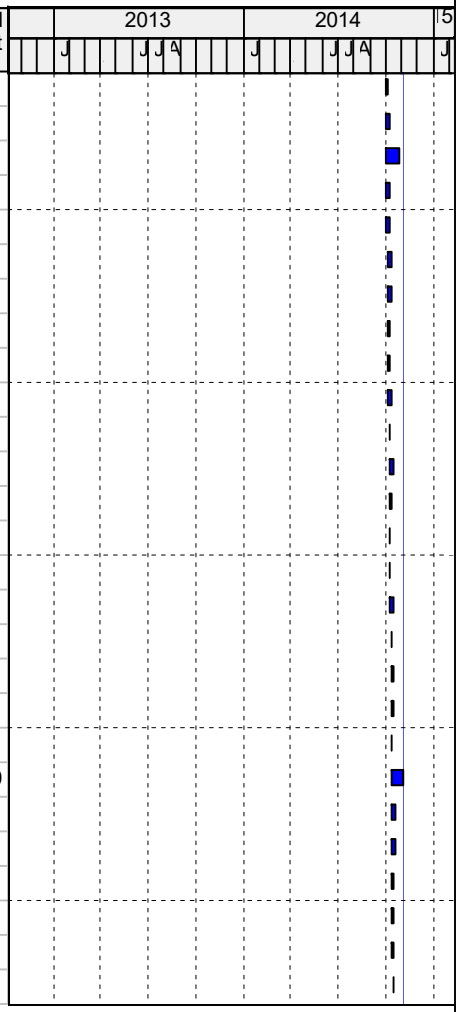



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8116 | Install Base and Door Thresholds | 5 | 0 | 15-Oct-14 A | 23-Oct-14 A | |
| L15-8112 | Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 16-Oct-14 A | |
| L04-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 2 | 16-Oct-14 A | 06-Nov-14 | 38 |
| L11-8124 | Install Flooring | 5 | 0 | 16-Oct-14 A | 22-Oct-14 A | |
| L17-8102S | Stock GWB | 1 | 0 | 17-Oct-14 A | 17-Oct-14 A | |
| L07-8126 | Install Doors | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |
| L09-8118 | Fire Alarm Trim | 2 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| L05-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 2 | 21-Oct-14 A | 13-Nov-14 | 33 |
| L08-8126 | Install Doors | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L10-8118 | Fire Alarm Trim | 2 | 0 | 21-Oct-14 A | 21-Oct-14 A | |
| L09-8126 | Install Doors | 2 | 0 | 22-Oct-14 A | 23-Oct-14 A | |
| L11-8118 | Fire Alarm Trim | 2 | 0 | 22-Oct-14 A | 22-Oct-14 A | |
| L06-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 2 | 23-Oct-14 A | 17-Nov-14 | 31 |
| L10-8126 | Install Doors | 2 | 0 | 23-Oct-14 A | 27-Oct-14 A | |
| L12-8124 | Install Flooring | 5 | 0 | 23-Oct-14 A | 29-Oct-14 A | |
| L12-8118 | Fire Alarm Trim | 2 | 0 | 23-Oct-14 A | 23-Oct-14 A | |
| L11-8116 | Install Base and Door Thresholds | 5 | 2 | 24-Oct-14 A | 04-Nov-14 | 20 |
| L07-8110 | HVAC Grilles & Registers | 2 | 0 | 27-Oct-14 A | 28-Oct-14 A | |
| L07-8120 | Bathrooms - Install Countertops | 3 | 1 | 27-Oct-14 A | 10-Nov-14 | 13 |
| L10-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |
| L11-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |
| L17-8102 | Hang GWB & Inspection | 4 | 1 | 27-Oct-14 A | 03-Nov-14 | 7 |
| L07-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 2 | 28-Oct-14 A | 18-Nov-14 | 30 |
| L08-8120 | Bathrooms - Install Countertops | 3 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L11-8126 | Install Doors | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L12-8108 | Lighting and Electrical Trim | 3 | 0 | 28-Oct-14 A | 30-Oct-14 A | |
| L12-8116 | Install Base and Door Thresholds | 5 | 4 | 28-Oct-14 A | 06-Nov-14 | 21 |

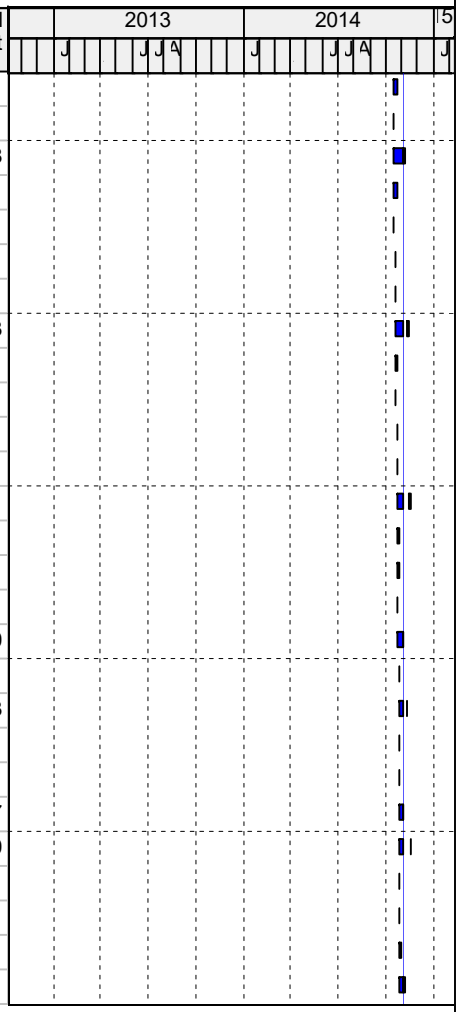



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8118 | Fire Alarm Trim | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L12-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L14-8108 | Lighting and Electrical Trim | 3 | 1 | 29-Oct-14 A | 13-Nov-14 | 17 |
| L14-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8118 | Fire Alarm Trim | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L04-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 2 | 30-Oct-14 A | 04-Nov-14 | 38 |
| L04-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 21 |
| L05-8120 | Bathrooms - Install Countertops | 3 | 3 | 03-Nov-14 | 05-Nov-14 | 13 |
| L08-8110 | HVAC Grilles & Registers | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 34 |
| L09-8110 | HVAC Grilles & Registers | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 36 |
| L10-8110 | HVAC Grilles & Registers | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 38 |
| L14-8124 | Install Flooring | 5 | 5 | 03-Nov-14 | 07-Nov-14 | 6 |
| L16-8104 | Paint - Prime | 2 | 2 | 03-Nov-14 | 04-Nov-14 | 6 |
| L03-8107 | Paint Final Coat | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 41 |
| L03-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 40 |
| L04-8107 | Paint Final Coat | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 26 |
| L05-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 19 |
| L06-8120 | Bathrooms - Install Countertops | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 13 |
| L06-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 19 |
| L11-8110 | HVAC Grilles & Registers | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 38 |
| L16-8105 | Paint - First Coat & Ceilings | 3 | 3 | 05-Nov-14 | 07-Nov-14 | 6 |
| L05-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 06-Nov-14 | 11-Nov-14 | 33 |
| L07-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 06-Nov-14 | 07-Nov-14 | 18 |
| L14-8116 | Install Base and Door Thresholds | 5 | 5 | 06-Nov-14 | 12-Nov-14 | 17 |
| L08-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 17 |
| L12-8110 | HVAC Grilles & Registers | 2 | 2 | 07-Nov-14 | 10-Nov-14 | 36 |

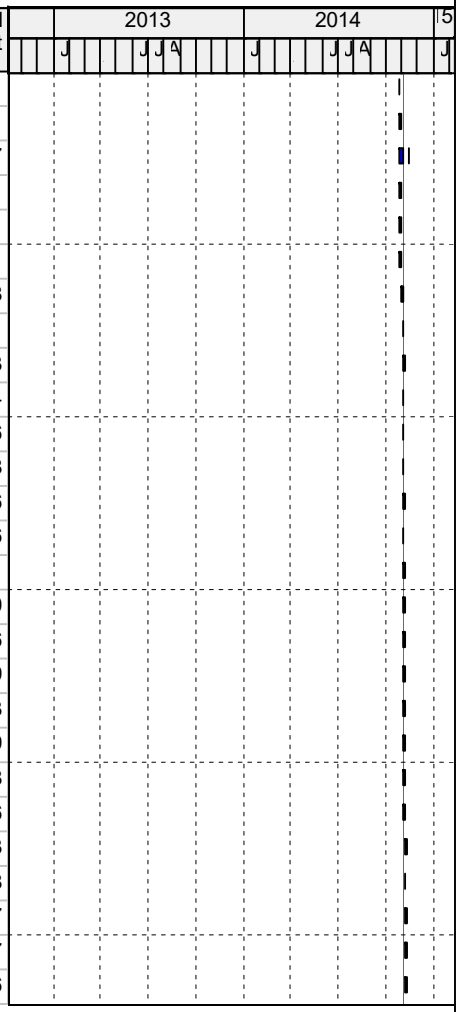


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8114 | Signage (By Owner) | 5 | 5 | 10-Nov-14 | 14-Nov-14 | 47 |
| L05-8107 | Paint Final Coat | 3 | 3 | 10-Nov-14 | 12-Nov-14 | 25 |
| L06-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 10-Nov-14 | 13-Nov-14 | 31 |
| L08-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 10-Nov-14 | 13-Nov-14 | 29 |
| L09-8120 | Bathrooms - Install Countertops | 3 | 3 | 10-Nov-14 | 12-Nov-14 | 13 |
| L09-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 16 |
| L15-8124 | Install Flooring | 5 | 5 | 10-Nov-14 | 14-Nov-14 | 6 |
| L17-8104 | Paint - Prime | 2 | 2 | 10-Nov-14 | 11-Nov-14 | 5 |
| L07-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 11-Nov-14 | 14-Nov-14 | 30 |
| L10-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 15 |
| L11-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 23 |
| L12-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 11-Nov-14 | 12-Nov-14 | 24 |
| L06-8107 | Paint Final Coat | 3 | 3 | 12-Nov-14 | 14-Nov-14 | 25 |
| L10-8120 | Bathrooms - Install Countertops | 3 | 3 | 12-Nov-14 | 14-Nov-14 | 13 |
| L17-8105 | Paint - First Coat & Ceilings | 3 | 3 | 12-Nov-14 | 14-Nov-14 | 5 |
| L07-8107 | Paint Final Coat | 3 | 3 | 13-Nov-14 | 17-Nov-14 | 26 |
| L09-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 13-Nov-14 | 18-Nov-14 | 26 |
| L15-8116 | Install Base and Door Thresholds | 5 | 5 | 13-Nov-14 | 19-Nov-14 | 10 |
| L08-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 14-Nov-14 | 19-Nov-14 | 29 |
| L14-8110 | HVAC Grilles & Registers | 2 | 2 | 14-Nov-14 | 17-Nov-14 | 32 |
| L08-8107 | Paint Final Coat | 3 | 3 | 17-Nov-14 | 19-Nov-14 | 26 |
| L10-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 17-Nov-14 | 20-Nov-14 | 24 |
| L11-8120 | Bathrooms - Install Countertops | 3 | 3 | 17-Nov-14 | 19-Nov-14 | 13 |
| L16-8124 | Install Flooring | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 6 |
| L14-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 18-Nov-14 | 19-Nov-14 | 20 |
| L09-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 19-Nov-14 | 24-Nov-14 | 26 |
| L09-8107 | Paint Final Coat | 3 | 3 | 19-Nov-14 | 21-Nov-14 | 26 |

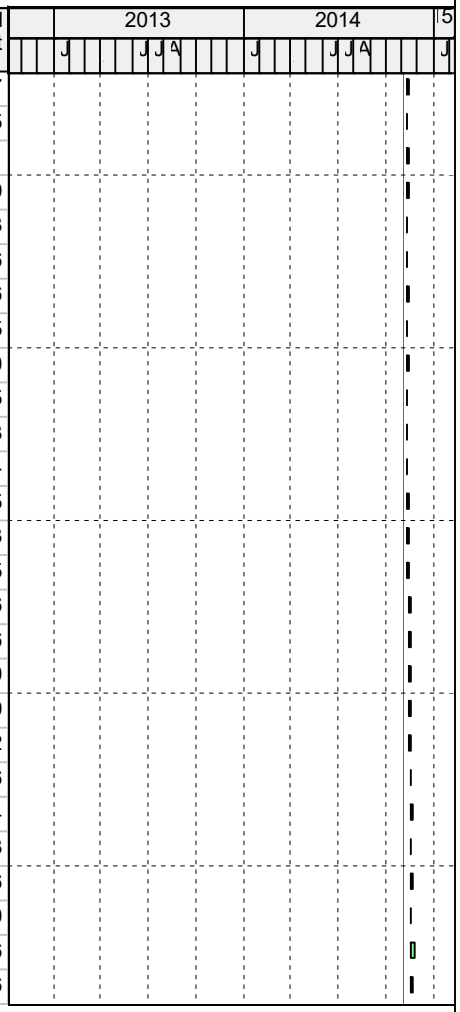



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8120 | Bathrooms - Install Countertops | 3 | 3 | 19-Nov-14 | 21-Nov-14 | 13 |
| L11-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 20-Nov-14 | 25-Nov-14 | 21 |
| L15-8108 | Lighting and Electrical Trim | 3 | 3 | 20-Nov-14 | 24-Nov-14 | 10 |
| L16-8112 | Fire Sprinkler Trim | 2 | 2 | 20-Nov-14 | 21-Nov-14 | 10 |
| L16-8116 | Install Base and Door Thresholds | 5 | 5 | 20-Nov-14 | 26-Nov-14 | 10 |
| L16-8118 | Fire Alarm Trim | 2 | 2 | 20-Nov-14 | 21-Nov-14 | 10 |
| L10-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 21-Nov-14 | 26-Nov-14 | 24 |
| L10-8107 | Paint Final Coat | 3 | 3 | 21-Nov-14 | 25-Nov-14 | 26 |
| L12-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 19 |
| L14-8120 | Bathrooms - Install Countertops | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 13 |
| L15-8120 | Bathrooms - Install Countertops | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 13 |
| L11-8107 | Paint Final Coat | 3 | 3 | 25-Nov-14 | 01-Dec-14 | 26 |
| L15-8110 | HVAC Grilles & Registers | 2 | 2 | 25-Nov-14 | 26-Nov-14 | 25 |
| L17-8124 | Install Flooring | 5 | 5 | 25-Nov-14 | 03-Dec-14 | 5 |
| L11-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 26-Nov-14 | 03-Dec-14 | 21 |
| L12-8107 | Paint Final Coat | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 25 |
| L14-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 01-Dec-14 | 04-Dec-14 | 16 |
| L15-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 01-Dec-14 | 04-Dec-14 | 16 |
| L15-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 14 |
| L16-8108 | Lighting and Electrical Trim | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 10 |
| L16-8120 | Bathrooms - Install Countertops | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 13 |
| L16-8126 | Install Doors | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 10 |
| L17-8112 | Fire Sprinkler Trim | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 5 |
| L17-8120 | Bathrooms - Install Countertops | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 13 |
| L17-8118 | Fire Alarm Trim | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 5 |
| L12-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 02-Dec-14 | 05-Dec-14 | 19 |
| L17-8116 | Install Base and Door Thresholds | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 5 |

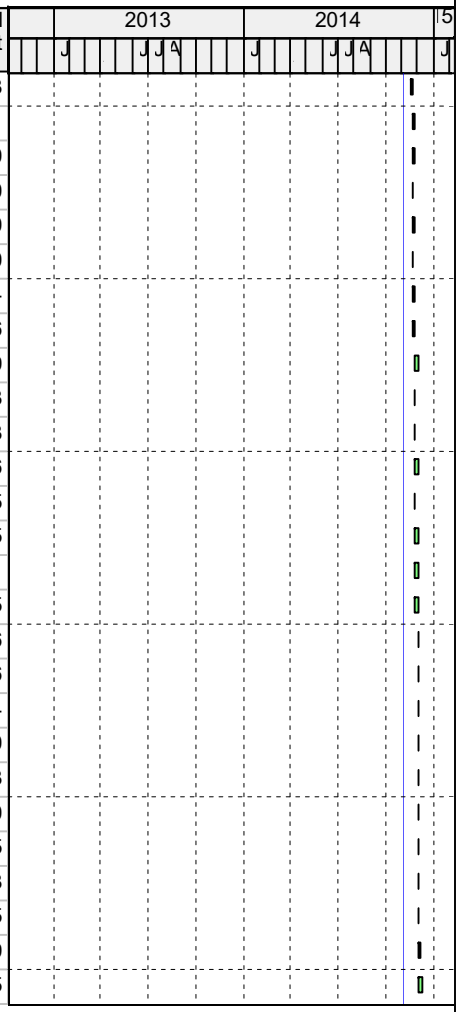



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8132 | Punchlist @ Guestrooms | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 26 |
| L04-8134 | Final Clean @ Guestrooms | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 26 |
| L14-8107 | Paint Final Coat | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 23 |
| L15-8107 | Paint Final Coat | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 23 |
| L03-8132 | Punchlist @ Guestrooms | 5 | 5 | 04-Dec-14 | 10-Dec-14 | 25 |
| L03-8134 | Final Clean @ Guestrooms | 5 | 5 | 04-Dec-14 | 10-Dec-14 | 25 |
| L04-8114 | Signage (By Owner) | 5 | 5 | 04-Dec-14 | 10-Dec-14 | 31 |
| L16-8110 | HVAC Grilles & Registers | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 21 |
| L16-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 04-Dec-14 | 09-Dec-14 | 14 |
| L17-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 04-Dec-14 | 09-Dec-14 | 13 |
| L14-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 05-Dec-14 | 10-Dec-14 | 16 |
| L15-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 05-Dec-14 | 10-Dec-14 | 16 |
| L05-8114 | Signage (By Owner) | 5 | 5 | 08-Dec-14 | 12-Dec-14 | 29 |
| L05-8132 | Punchlist @ Guestrooms | 5 | 5 | 08-Dec-14 | 12-Dec-14 | 23 |
| L05-8134 | Final Clean @ Guestrooms | 5 | 5 | 08-Dec-14 | 12-Dec-14 | 23 |
| L06-8132 | Punchlist @ Guestrooms | 5 | 5 | 08-Dec-14 | 12-Dec-14 | 23 |
| L06-8134 | Final Clean @ Guestrooms | 5 | 5 | 08-Dec-14 | 12-Dec-14 | 23 |
| L16-8107 | Paint Final Coat | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 21 |
| L16-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 08-Dec-14 | 09-Dec-14 | 10 |
| L17-8108 | Lighting and Electrical Trim | 3 | 3 | 09-Dec-14 | 11-Dec-14 | 5 |
| L17-8126 | Install Doors | 2 | 2 | 09-Dec-14 | 10-Dec-14 | 7 |
| L06-8114 | Signage (By Owner) | 5 | 5 | 10-Dec-14 | 16-Dec-14 | 27 |
| L16-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 10-Dec-14 | 15-Dec-14 | 14 |
| L17-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 10-Dec-14 | 15-Dec-14 | 13 |
| L07-8132 | Punchlist @ Guestrooms | 5 | 5 | 11-Dec-14 | 17-Dec-14 | 20 |
| L07-8134 | Final Clean @ Guestrooms | 5 | 5 | 11-Dec-14 | 17-Dec-14 | 20 |
| L08-8132 | Punchlist @ Guestrooms | 5 | 5 | 11-Dec-14 | 17-Dec-14 | 20 |

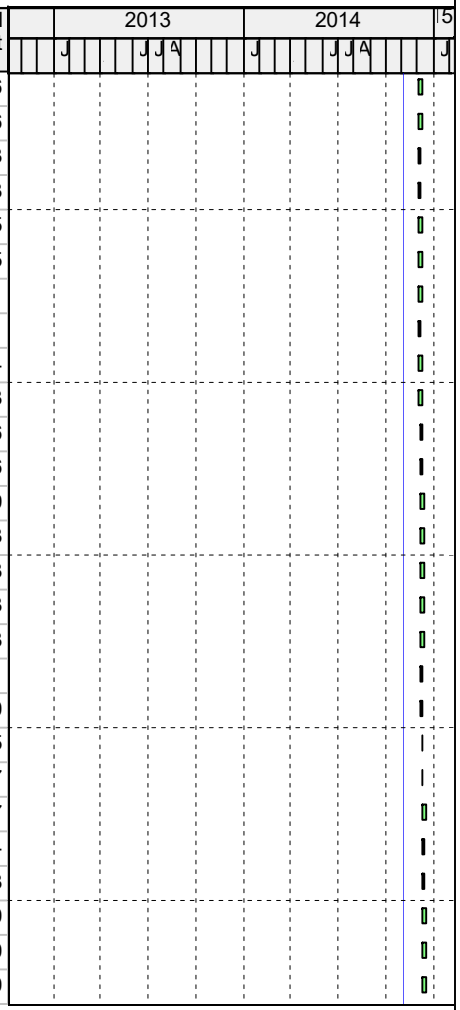



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8134 | Final Clean @ Guestrooms | 5 | 5 | 11-Dec-14 | 17-Dec-14 | 20 |
| L07-8114 | Signage (By Owner) | 5 | 5 | 12-Dec-14 | 18-Dec-14 | 25 |
| L17-8110 | HVAC Grilles & Registers | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 14 |
| L08-8114 | Signage (By Owner) | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 23 |
| L09-8132 | Punchlist @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 17 |
| L09-8134 | Final Clean @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 17 |
| L10-8132 | Punchlist @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 17 |
| L10-8134 | Final Clean @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 17 |
| L17-8107 | Paint - Final Coat | 3 | 3 | 16-Dec-14 | 18-Dec-14 | 14 |
| L17-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 16-Dec-14 | 17-Dec-14 | 5 |
| L09-8114 | Signage (By Owner) | 5 | 5 | 18-Dec-14 | 24-Dec-14 | 21 |
| L11-8132 | Punchlist @ Guestrooms | 5 | 5 | 19-Dec-14 | 29-Dec-14 | 14 |
| L11-8134 | Final Clean @ Guestrooms | 5 | 5 | 19-Dec-14 | 29-Dec-14 | 14 |
| L12-8132 | Punchlist @ Guestrooms | 5 | 5 | 19-Dec-14 | 29-Dec-14 | 14 |
| L12-8134 | Final Clean @ Guestrooms | 5 | 5 | 19-Dec-14 | 29-Dec-14 | 14 |
| L10-8114 | Signage (By Owner) | 5 | 5 | 22-Dec-14 | 30-Dec-14 | 19 |
| L12-8114 | Signage (By Owner) | 5 | 5 | 23-Dec-14 | 31-Dec-14 | 18 |
| L11-8114 | Signage (By Owner) | 5 | 5 | 24-Dec-14 | 02-Jan-15 | 17 |
| L14-8132 | Punchlist @ Guestrooms | 5 | 5 | 24-Dec-14 | 02-Jan-15 | 11 |
| L14-8134 | Final Clean @ Guestrooms | 5 | 5 | 24-Dec-14 | 02-Jan-15 | 11 |
| L15-8132 | Punchlist @ Guestrooms | 5 | 5 | 24-Dec-14 | 02-Jan-15 | 11 |
| L15-8134 | Final Clean @ Guestrooms | 5 | 5 | 24-Dec-14 | 02-Jan-15 | 11 |
| L14-8114 | Signage (By Owner) | 5 | 5 | 29-Dec-14 | 05-Jan-15 | 16 |
| L15-8114 | Signage (By Owner) | 5 | 5 | 29-Dec-14 | 05-Jan-15 | 16 |
| L16-8114 | Signage (By Owner) | 5 | 5 | 31-Dec-14 | 07-Jan-15 | 14 |
| L16-8132 | Punchlist @ Guestrooms | 5 | 5 | 31-Dec-14 | 06-Jan-15 | 11 |
| L16-8134 | Final Clean @ Guestrooms | 5 | 5 | 31-Dec-14 | 06-Jan-15 | 11 |

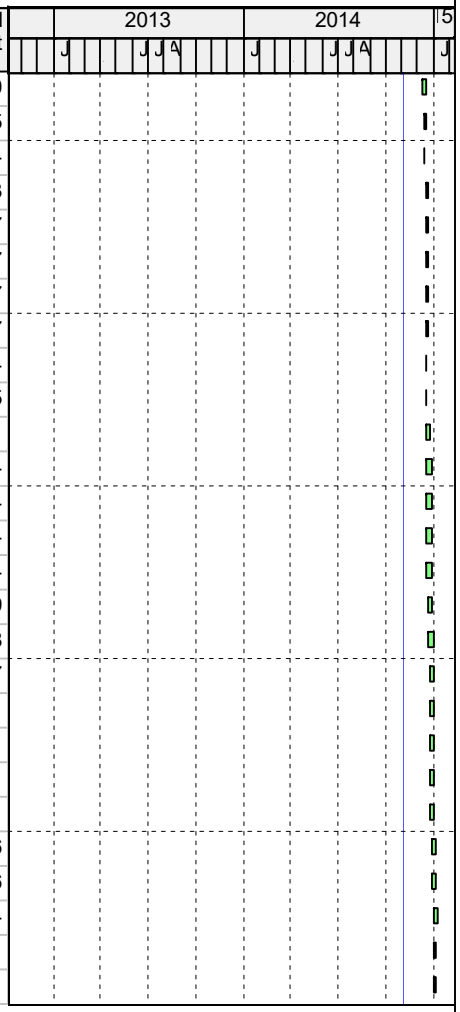



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8114 | Signage (By Owner) | 5 | 5 | 31-Dec-14 | 07-Jan-15 | 14 |
| L17-8132 | Punchlist @ Guestrooms | 5 | 5 | 31-Dec-14 | 07-Jan-15 | 8 |
| L17-8134 | Final Clean @ Guestrooms | 5 | 5 | 31-Dec-14 | 07-Jan-15 | 8 |
| **Pool Area** | | | | | | |
| L03-8216 | Pool - Install tile, coping and depth markers | 10 | 10 | 03-Nov-14 | 14-Nov-14 | 13 |
| L03-8218 | Pool - Install pool equipment | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 13 |
| **Corridors / Common / Public Areas** | | | | | | |
| L03-8200 | Vinyl Wall Coverings | 3 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L04-8200 | Vinyl Wall Coverings | 5 | 0 | 06-Aug-14 A | 12-Aug-14 A | |
| L05-8200 | Vinyl Wall Coverings | 5 | 0 | 12-Aug-14 A | 22-Sep-14 A | |
| L03-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L06-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L08-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 11-Sep-14 A | 19-Sep-14 A | |
| L04-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| L05-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L06-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L07-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L09-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| L10-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 08-Oct-14 A | |
| L11-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 10-Oct-14 A | |
| L08-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L12-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| L09-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L14-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 16-Oct-14 A | 27-Oct-14 A | |
| L10-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |
| L11-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |

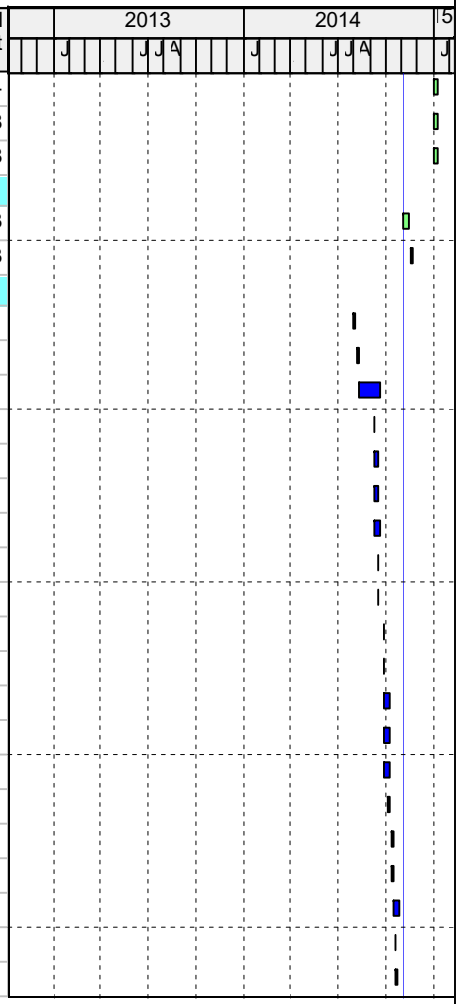


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 22-Oct-14 A | 29-Oct-14 A | |
| L12-8202 | Corridors - Lighting and Electrical Trim | 2 | 2 | 05-Nov-14 | 06-Nov-14 | 24 |
| L14-8202 | Corridors - Lighting and Electrical Trim | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 20 |
| L16-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 4 | 12-Nov-14 | 17-Nov-14 | 6 |
| L17-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 4 | 19-Nov-14 | 24-Nov-14 | 5 |
| L15-8202 | Corridors - Lighting and Electrical Trim | 2 | 2 | 21-Nov-14 | 24-Nov-14 | 14 |
| L04-8206 | Corridors - Flooring & Base | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 13 |
| L16-8202 | Corridors - Lighting and Electrical Trim | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 10 |
| L05-8206 | Corridors - Flooring & Base | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 13 |
| L06-8206 | Corridors - Flooring & Base | 3 | 3 | 05-Dec-14 | 09-Dec-14 | 13 |
| L07-8206 | Corridors - Flooring & Base | 3 | 3 | 09-Dec-14 | 11-Dec-14 | 13 |
| L04-8208 | Final Clean (Entire Floor) | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 26 |
| L04-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 10-Dec-14 | 10-Dec-14 | 26 |
| L17-8202 | Corridors - Lighting and Electrical Trim | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 5 |
| L04-8212 | Resolve Final Punchlist | 5 | 5 | 11-Dec-14 | 17-Dec-14 | 26 |
| L08-8206 | Corridors - Flooring & Base | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 13 |
| L05-8208 | Final Clean (Entire Floor) | 2 | 2 | 15-Dec-14 | 16-Dec-14 | 23 |
| L05-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 15-Dec-14 | 15-Dec-14 | 23 |
| L06-8208 | Final Clean (Entire Floor) | 2 | 2 | 15-Dec-14 | 16-Dec-14 | 23 |
| L06-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 15-Dec-14 | 15-Dec-14 | 23 |
| L09-8206 | Corridors - Flooring & Base | 3 | 3 | 15-Dec-14 | 17-Dec-14 | 13 |
| L05-8212 | Resolve Final Punchlist | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 23 |
| L06-8212 | Resolve Final Punchlist | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 23 |
| L10-8206 | Corridors - Flooring & Base | 3 | 3 | 17-Dec-14 | 19-Dec-14 | 13 |
| L04-8214 | Floor Complete | 0 | 0 | | 17-Dec-14 | 26 |
| L03-8206 | Corridors - Flooring & Base | 3 | 3 | 18-Dec-14 | 20-Dec-14 | 23 |
| L07-8208 | Final Clean (Entire Floor) | 2 | 2 | 18-Dec-14 | 19-Dec-14 | 20 |

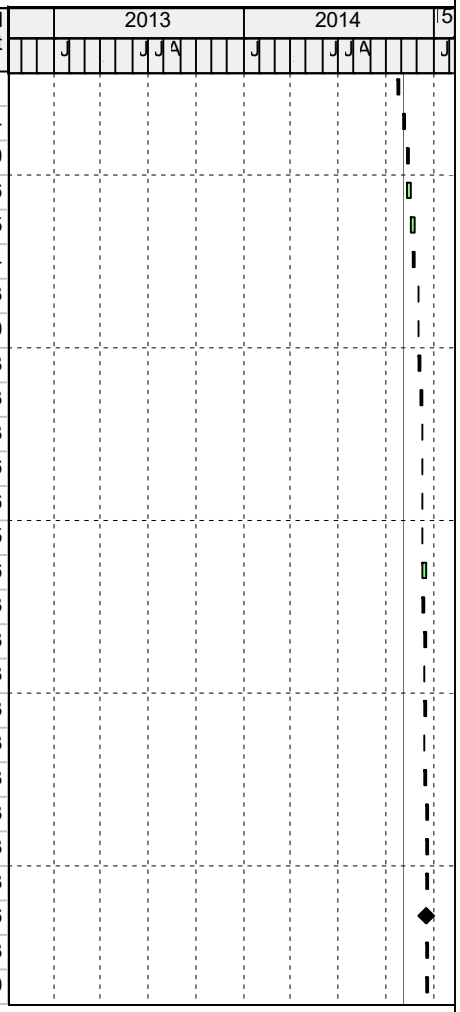



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 18-Dec-14 | 18-Dec-14 | 20 |
| L08-8208 | Final Clean (Entire Floor) | 2 | 2 | 18-Dec-14 | 19-Dec-14 | 20 |
| L08-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 18-Dec-14 | 18-Dec-14 | 20 |
| L07-8212 | Resolve Final Punchlist | 5 | 5 | 19-Dec-14 | 29-Dec-14 | 20 |
| L08-8212 | Resolve Final Punchlist | 5 | 5 | 19-Dec-14 | 29-Dec-14 | 20 |
| L11-8206 | Corridors - Flooring & Base | 3 | 3 | 19-Dec-14 | 23-Dec-14 | 13 |
| L12-8206 | Corridors - Flooring & Base | 3 | 3 | 19-Dec-14 | 22-Dec-14 | 17 |
| L14-8206 | Corridors - Flooring & Base | 3 | 3 | 22-Dec-14 | 24-Dec-14 | 17 |
| L15-8206 | Corridors - Flooring & Base | 3 | 3 | 22-Dec-14 | 24-Dec-14 | 17 |
| L05-8214 | Floor Complete | 0 | 0 | | 22-Dec-14 | 23 |
| L06-8214 | Floor Complete | 0 | 0 | | 22-Dec-14 | 23 |
| L09-8208 | Final Clean (Entire Floor) | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 17 |
| L09-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 23-Dec-14 | 23-Dec-14 | 17 |
| L09-8212 | Resolve Final Punchlist | 5 | 5 | 24-Dec-14 | 02-Jan-15 | 17 |
| L10-8208 | Final Clean (Entire Floor) | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 16 |
| L10-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 24-Dec-14 | 24-Dec-14 | 16 |
| L16-8206 | Corridors - Flooring & Base | 3 | 3 | 24-Dec-14 | 30-Dec-14 | 13 |
| L17-8206 | Corridors - Flooring & Base | 3 | 3 | 24-Dec-14 | 30-Dec-14 | 13 |
| L10-8212 | Resolve Final Punchlist | 5 | 5 | 29-Dec-14 | 05-Jan-15 | 16 |
| L07-8214 | Floor Complete | 0 | 0 | | 29-Dec-14 | 20 |
| L08-8214 | Floor Complete | 0 | 0 | | 29-Dec-14 | 20 |
| L11-8208 | Final Clean (Entire Floor) | 2 | 2 | 30-Dec-14 | 31-Dec-14 | 14 |
| L11-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 30-Dec-14 | 30-Dec-14 | 14 |
| L12-8208 | Final Clean (Entire Floor) | 2 | 2 | 30-Dec-14 | 31-Dec-14 | 14 |
| L12-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 30-Dec-14 | 30-Dec-14 | 14 |
| L03-8208 | Final Clean (Entire Floor) | 2 | 2 | 31-Dec-14 | 02-Jan-15 | 13 |
| L03-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 31-Dec-14 | 31-Dec-14 | 13 |

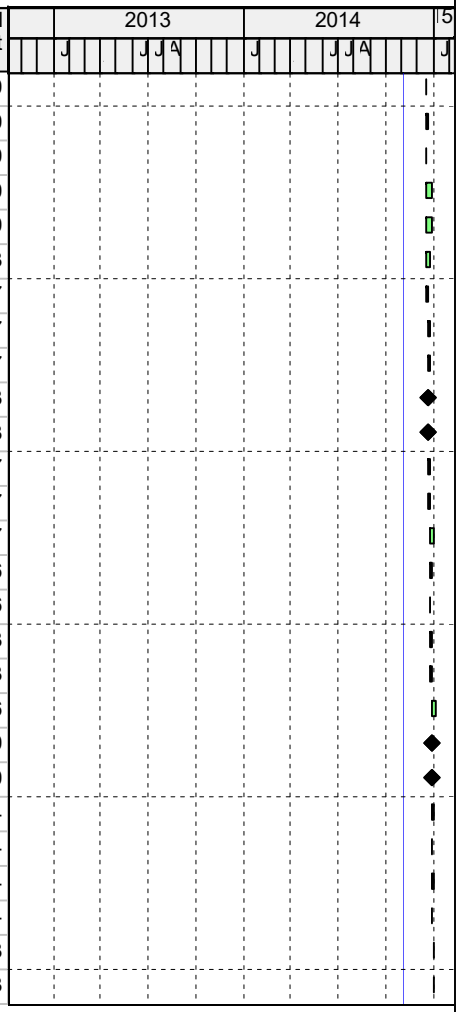



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8212 | Resolve Final Punchlist | 5 | 5 | 31-Dec-14 | 07-Jan-15 | 14 |
| L12-8212 | Resolve Final Punchlist | 5 | 5 | 31-Dec-14 | 07-Jan-15 | 14 |
| L03-8212 | Resolve Final Punchlist | 5 | 5 | 02-Jan-15 | 08-Jan-15 | 13 |
| L09-8214 | Floor Complete | 0 | 0 | | 02-Jan-15 | 17 |
| L14-8208 | Final Clean (Entire Floor) | 2 | 2 | 05-Jan-15 | 06-Jan-15 | 11 |
| L14-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 05-Jan-15 | 05-Jan-15 | 11 |
| L15-8208 | Final Clean (Entire Floor) | 2 | 2 | 05-Jan-15 | 06-Jan-15 | 11 |
| L15-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 05-Jan-15 | 05-Jan-15 | 11 |
| L10-8214 | Floor Complete | 0 | 0 | | 05-Jan-15 | 16 |
| L14-8212 | Resolve Final Punchlist | 5 | 5 | 06-Jan-15 | 12-Jan-15 | 11 |
| L15-8212 | Resolve Final Punchlist | 5 | 5 | 06-Jan-15 | 12-Jan-15 | 11 |
| L16-8208 | Final Clean (Entire Floor) | 2 | 2 | 07-Jan-15 | 08-Jan-15 | 9 |
| L16-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 07-Jan-15 | 07-Jan-15 | 9 |
| L11-8214 | Floor Complete | 0 | 0 | | 07-Jan-15 | 14 |
| L12-8214 | Floor Complete | 0 | 0 | | 07-Jan-15 | 14 |
| L16-8212 | Resolve Final Punchlist | 5 | 5 | 08-Jan-15 | 14-Jan-15 | 9 |
| L17-8208 | Final Clean (Entire Floor) | 2 | 2 | 08-Jan-15 | 09-Jan-15 | 8 |
| L17-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 08-Jan-15 | 08-Jan-15 | 8 |
| L03-8214 | Floor Complete | 0 | 0 | | 08-Jan-15 | 13 |
| L17-8212 | Resolve Final Punchlist | 5 | 5 | 09-Jan-15 | 15-Jan-15 | 8 |
| L14-8214 | Floor Complete | 0 | 0 | | 12-Jan-15 | 11 |
| L15-8214 | Floor Complete | 0 | 0 | | 12-Jan-15 | 11 |
| L16-8214 | Floor Complete | 0 | 0 | | 14-Jan-15 | 9 |
| L17-8214 | Floor Complete | 0 | 0 | | 15-Jan-15 | 8 |
| **Mech Penthouse** | | | | | | |
| PH-8100 | PH - Insulation & Vapor Barrier | 5 | 0 | 09-Oct-14 A | 13-Oct-14 A | |
| PH-8102 | PH - Complete GWB Hang / Tape / Finish | 6 | 3 | 14-Oct-14 A | 05-Nov-14 | 37 |

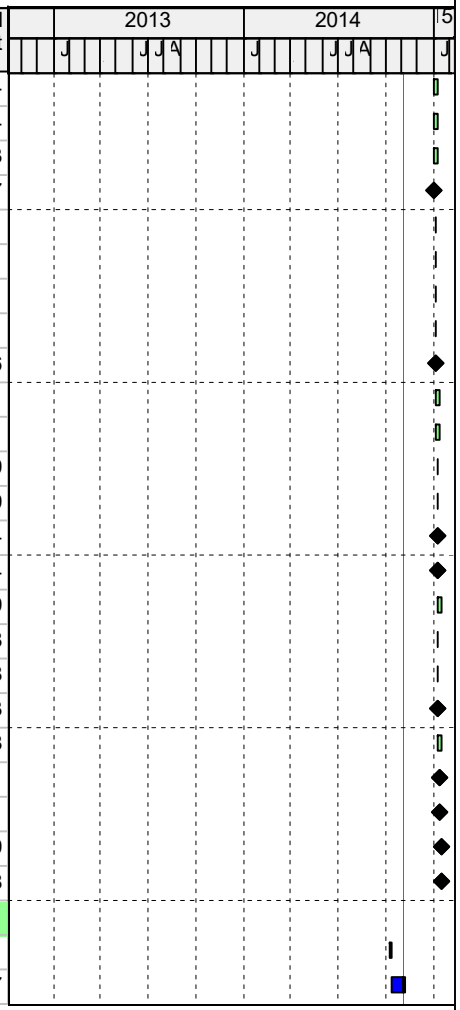



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-8104 | PH - Int Painting | 4 | 4 | 06-Nov-14 | 11-Nov-14 | 37 |
| PH-8122 | PH - Plumbing Trim / Finish | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 42 |
| PH-8108 | PH - Elec Trim / Finish | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 37 |
| PH-8110 | PH - HVAC Trim / Finish | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 37 |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 37 |
| PH-8114 | PH - Install Stairs to Roof | 1 | 1 | 12-Nov-14 | 12-Nov-14 | 47 |
| PH-8126 | PH - Doors & Hardware | 2 | 2 | 12-Nov-14 | 13-Nov-14 | 43 |
| PH-8118 | PH - Elec Specialties Trim / Finish | 5 | 5 | 12-Nov-14 | 18-Nov-14 | 37 |
| PH-8124 | PH - Flooring | 5 | 5 | 17-Nov-14 | 21-Nov-14 | 37 |
| PH-8132 | PH - Contractor Pre-Punchlist | 1 | 1 | 24-Nov-14 | 24-Nov-14 | 39 |
| PH-8134 | PH - Final Trims and Touch-Up | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 37 |
| PH-8208 | PH - Final Clean | 1 | 1 | 01-Dec-14 | 01-Dec-14 | 37 |
| PH-8212 | PH - Final Punchlist | 1 | 1 | 02-Dec-14 | 02-Dec-14 | 37 |
| PH-8214 | PH - Floor Complete | 0 | 0 | | 02-Dec-14 | 37 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| Smoke Control | | | | | | |
| CO-7104 | Smoke Control Pre-Testing (Podium) | 12 | 12 | 02-Jan-15 | 19-Jan-15 | 1 |
| CO-7106 | City of Bellevue Smoke Control Testing (Podium) | 5 | 5 | 20-Jan-15 | 26-Jan-15 | 1 |
| CO-7108 | Final Marriott Smoke Control Testing | 5 | 5 | 27-Jan-15 | 02-Feb-15 | 1 |
| Fire Sprinklers | | | | | | |
| CO-7110 | Fire Sprinkler Pre-Testing (Podium) | 12 | 12 | 02-Jan-15 | 19-Jan-15 | 1 |
| CO-7112 | City of Bellevue Fire Sprinkler Inspection / Approval (F | 5 | 5 | 20-Jan-15 | 26-Jan-15 | 1 |
| CO-7114 | Marriott Fire Sprinkler Testing | 5 | 5 | 27-Jan-15 | 02-Feb-15 | 1 |
| Fire Alarm | | | | | | |
| CO-7116 | Fire Alarm Pre-Testing (Podium) | 12 | 12 | 02-Jan-15 | 19-Jan-15 | 1 |
| CO-7118 | City of Bellevue Fire Alarm Inspection / Approval (Pod | 5 | 5 | 20-Jan-15 | 26-Jan-15 | 1 |
| CO-7120 | Marriott Fire Alarm Testing | 5 | 5 | 27-Jan-15 | 02-Feb-15 | 1 |

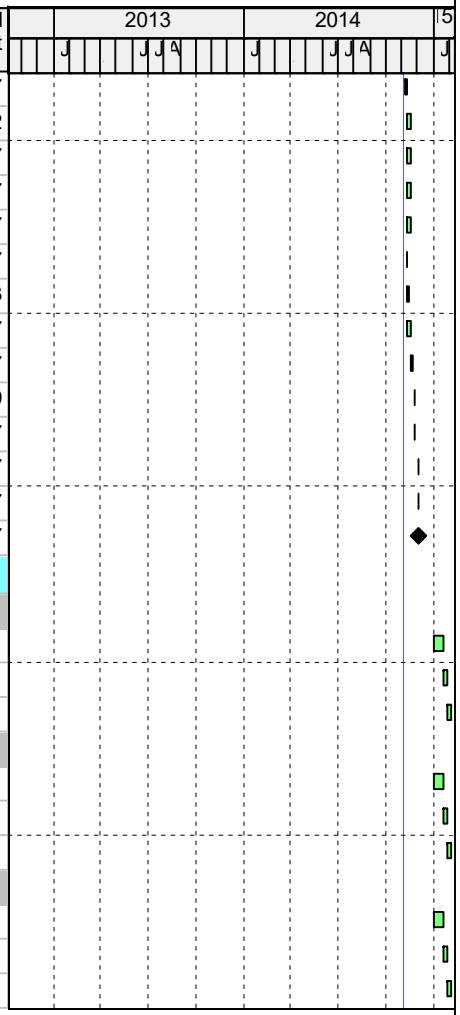


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Start-Up / Testing / Commissioning** | | | | | | |
| CO-7100 | Cx - Equipment Start-Up & Testing, Podium | 15 | 15 | 19-Nov-14 | 11-Dec-14 | 13 |
| CO-7102 | Cx - DDC Point-To-Point Checks, Podium | 10 | 10 | 26-Nov-14 | 11-Dec-14 | 30 |





© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Working Schedule - 11-23-14 Update** | | | | | | |
| L09-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-04 A | 30-Sep-14 A | |
| I-1500 | Owner release revised LV design - Tower (ASIs 5, 13, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-1550 | Owner release revised LV design - Podium (ASIs 5, 1 | 200 | 0 | 23-May-13 A | 28-Apr-14 A | |
| I-1900 | Owner issue design revisions (ASIs 4, 9, 19, 34) | 215 | 0 | 23-May-13 A | 24-Mar-14 A | |
| I-2500 | Owner issue LL1 electrical revisions (ASIs 7, 9r2, 14, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-3400 | Owner provide Level 2 ceiling heights | 180 | 0 | 24-Jun-13 A | 24-Mar-14 A | |
| I-3700 | Owner resolve wall condition between stair and Eleva | 200 | 0 | 27-Jun-13 A | 16-Jun-14 A | |
| MM-1000 | MM - Temporary Power Available | 0 | 0 | 08-Jul-13 A | | |
| I-2100 | Owner revise roof steel design (Submittals 365, 370, | 200 | 0 | 09-Jul-13 A | 07-Apr-14 A | |
| I-2200 | Owner resolve elevator steel issue (RFI 112, RFI 112. | 200 | 0 | 09-Jul-13 A | 03-Mar-14 A | |
| I-2400 | Owner provide Tower light fixture selections (ASI 36) | 185 | 0 | 18-Jul-13 A | 08-Apr-14 A | |
| I-2900 | Owner revise Food Service and Kitchen (ASIs 11, 12, | 140 | 0 | 08-Aug-13 A | 27-Feb-14 A | |
| I-1400 | Owner develop envelope redesign | 70 | 0 | 27-Aug-13 A | 12-Dec-13 A | |
| I-3600 | Owner closeout glass/glazing allowance | 160 | 0 | 04-Sep-13 A | 30-Apr-14 A | |
| I-1200 | Owner release revised Concierge Lounge design (AS | 160 | 0 | 06-Sep-13 A | 08-Apr-14 A | |
| I-2800 | Owner revise interior public space design (ASIs 16, 18 | 130 | 0 | 25-Sep-13 A | 09-Apr-14 A | |
| I-2000 | Owner approve door frames (Submittals 258, 454, 48 | 85 | 0 | 27-Sep-13 A | 23-Jan-14 A | |
| I-3100 | Owner revise ballroom ceiling design (ASIs 18, 25) | 100 | 0 | 17-Oct-13 A | 25-Feb-14 A | |
| I-1600 | Owner provide directive for south & east corridor encl | 110 | 0 | 28-Oct-13 A | 18-Apr-14 A | |
| I-2300 | Owner resolve fire smoke dampers issue (RFI 233) | 115 | 0 | 30-Oct-13 A | 11-Apr-14 A | |
| I-2600 | Owner resolve L2 slab coordination issue | 4 | 0 | 13-Nov-13 A | 16-Nov-13 A | |
| I-2700 | Owner revise tower guest rooms design (ASIs 23, 29) | 58 | 0 | 04-Dec-13 A | 26-Feb-14 A | |
| I-1700 | Owner provide design for dry site utilities (ASIs 20, 20 | 66 | 0 | 09-Dec-13 A | 13-Mar-14 A | |
| I-1402 | Begin exterior panel production | 41 | 0 | 13-Dec-13 A | 12-Feb-14 A | |
| I-1300 | Owner issue "Hold" directive (email) | 0 | 0 | | 19-Dec-13 A | |
| I-1100 | Owner release revised L17 design (ASI 23, 29R1) | 74 | 0 | 20-Dec-13 A | 08-Apr-14 A | |

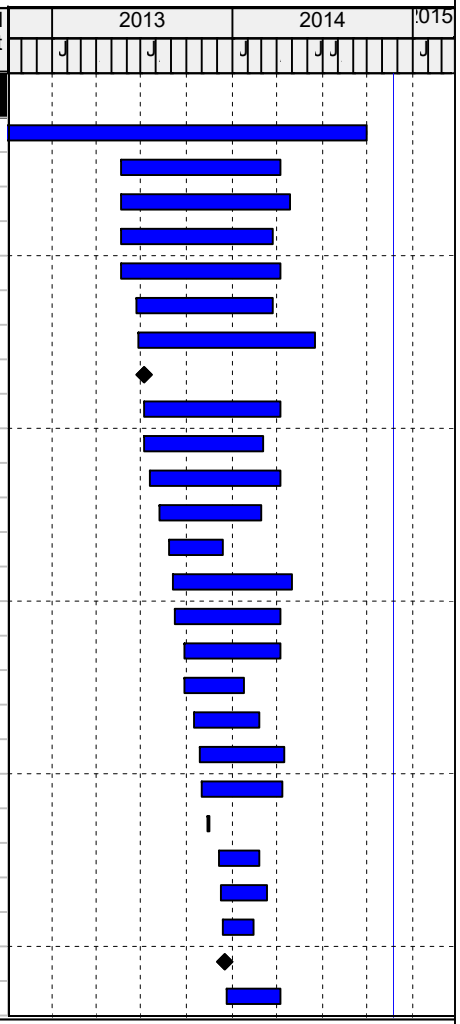


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1302 | Owner issue ASI 30 (Prep Kitchen Revisions) | 47 | 0 | 20-Dec-13 A | 27-Feb-14 A | |
| I-1404 | City of Bellevue Approval | 90 | 0 | 23-Dec-13 A | 15-Jul-14 A | |
| I-3000 | Owner revise bar area (change to straight bar, IDRFI-( | 71 | 0 | 22-Jan-14 A | 27-May-14 A | |
| I-1306 | Prep Kitchen - Additional plumbing (ASI 30) | 4 | 0 | 17-Feb-14 A | 01-Aug-14 A | |
| I-2202 | Fabricate revised elevator steel | 60 | 0 | 04-Mar-14 A | 07-May-14 A | |
| I-2704 | Framing "Go Back" work for ASIs 23, 29 - L4 | 1 | 0 | 05-Mar-14 A | 12-Mar-14 A | |
| I-3900 | RFI 471, Resolve Ballroom parapet height issue | 1 | 0 | 08-Mar-14 A | 07-May-14 A | |
| I-1702 | Owner provide directive to proceed | 26 | 0 | 14-Mar-14 A | 01-May-14 A | |
| I-3300 | Owner provide Guest Room plumbing fixture selectio | 1 | 0 | 20-Mar-14 A | 20-Mar-14 A | |
| I-1902 | Procure revised structural steel | 15 | 0 | 25-Mar-14 A | 14-Apr-14 A | |
| I-4000 | Owner complete design of east stitched enclosure (fo | 1 | 0 | 01-Apr-14 A | 14-May-14 A | |
| I-2102 | Fabricate revised roof steel | 20 | 0 | 08-Apr-14 A | 15-May-14 A | |
| I-3200 | Owner provide light fixture selections for podium level | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| I-3800 | Resolve Heat Pump Electrical Overcurrent Issue | 20 | 0 | 23-Apr-14 A | 18-Jun-14 A | |
| L10-8221 | HVAC Risers Duct Insulation | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L11-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| I-2304 | Framing "Go Back" work at L3 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2306 | Framing "Go Back" work at L4 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2308 | Framing "Go Back" work at L5 for RFI 233 | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2706 | Framing "Go Back" work for ASIs 23, 29 - L5 | 1 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2708 | Framing "Go Back" work for ASIs 23, 29 - L6 | 1 | 0 | 29-Apr-14 A | 09-May-14 A | |
| I-2702 | Framing "Go Back" work for ASIs 23, 29 - L3 | 1 | 0 | 01-May-14 A | 01-May-14 A | |
| I-1706 | PSE scheduling delay | 10 | 0 | 01-May-14 A | 20-May-14 A | |
| I-3602 | Complete shop drawings & fab/deliver storefront fram | 40 | 0 | 01-May-14 A | 14-Jun-14 A | |
| L04-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| I-1802 | Rework framing for door hold-opens - LL4 | 1 | 0 | 07-May-14 A | 08-May-14 A | |

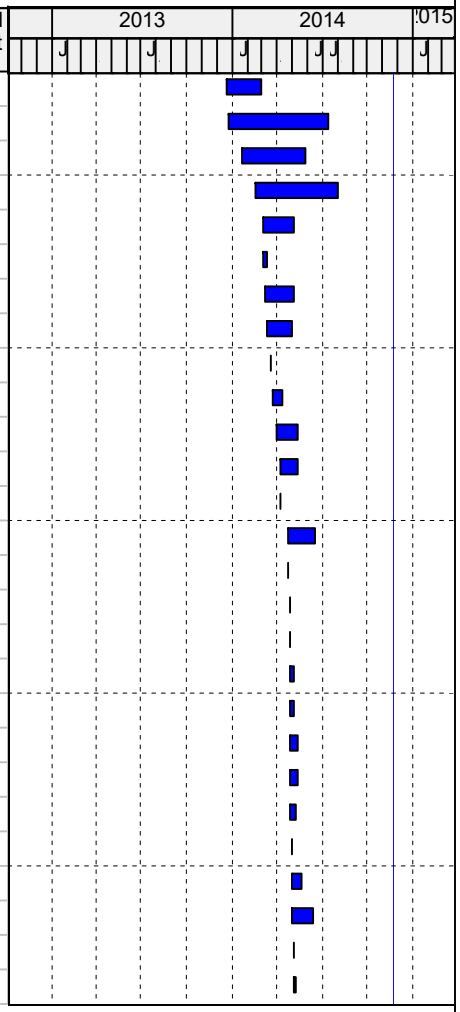


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-May-14 A | 12-May-14 A | |
| I-1800 | Owner issue directive to proceed with door hold-open | 1 | 0 | 08-May-14 A | 08-May-14 A | |
| I-1804 | Rework framing for door hold-opens - LL3 | 1 | 0 | 08-May-14 A | 09-May-14 A | |
| I-2312 | Framing "Go Back" work at L7 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-2314 | Framing "Go Back" work at L8 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-3902 | Install Ballroom parapet extension | 5 | 0 | 08-May-14 A | 13-May-14 A | |
| I-1806 | Rework framing for door hold-opens - LL2 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-1808 | Rework framing for door hold-opens - LL1 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-2310 | Framing "Go Back" work at L6 for RFI 233 | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| I-2710 | Framing "Go Back" work for ASIs 23, 29 - L7 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| L05-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L06-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L05-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| LL2E-8110 | LL2 - Electrical, Fire pumps/equipment final connectic | 5 | 0 | 12-May-14 A | 30-Oct-14 A | |
| PH-8704 | PH - Install Machine Support Steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| PH-8710 | Install elevator rail support steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| L03-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L03-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 13-May-14 A | 14-May-14 A | |
| I-4002 | East Stitched - Install framing and windows | 9 | 0 | 19-May-14 A | 09-Jun-14 A | |
| L10-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L11-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L12-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| RF-4038 | AR - Concrete pads and curbs | 5 | 0 | 21-May-14 A | 04-Jun-14 A | |
| L10-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L11-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L12-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |

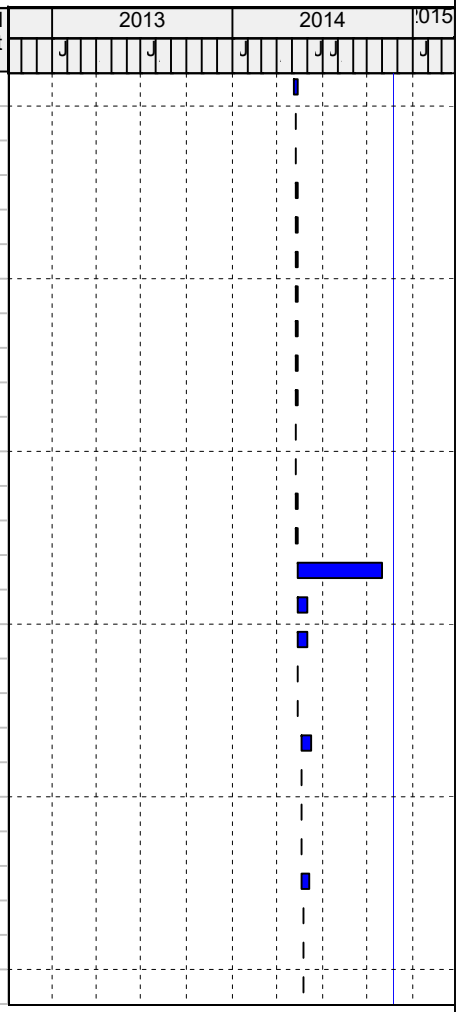



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L15-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 27-May-14 A | |
| L11-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 07-Jun-14 A | |
| L12-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 27-May-14 A | 06-Jun-14 A | |
| I-3002 | City of Bellevue approve bar design changes. | 5 | 2 | 28-May-14 A | 25-Nov-14 | 21 |
| L16-8221 | HVAC Risers Duct Insulation | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| PH-8712 | PH - Complete Framing and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| PH-8714 | Stage PH/L18 roofing materials | 2 | 0 | 30-May-14 A | 30-May-14 A | |
| L08-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L08-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 02-Jun-14 A | 20-Jun-14 A | |
| PH-8704I | Correct support steel embeds | 2 | 0 | 02-Jun-14 A | 11-Jun-14 A | |
| L14-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 03-Jun-14 A | 04-Jun-14 A | |
| L17-8221 | HVAC Risers Duct Insulation | 1 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| PC-4010 | PC - Fireproof Entry Roof Steel | 5 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| I-4100 | Owner resolve trap primers issue (RFI 560) | 5 | 0 | 03-Jun-14 A | 20-Jun-14 A | |
| RF-6028 | Tower Roof - Structural Steel | 5 | 0 | 04-Jun-14 A | 17-Jun-14 A | |
| L14-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L1B-6005 | Head of Wall Fire Caulk at CMU (including East Servi | 2 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L14-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L15-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |

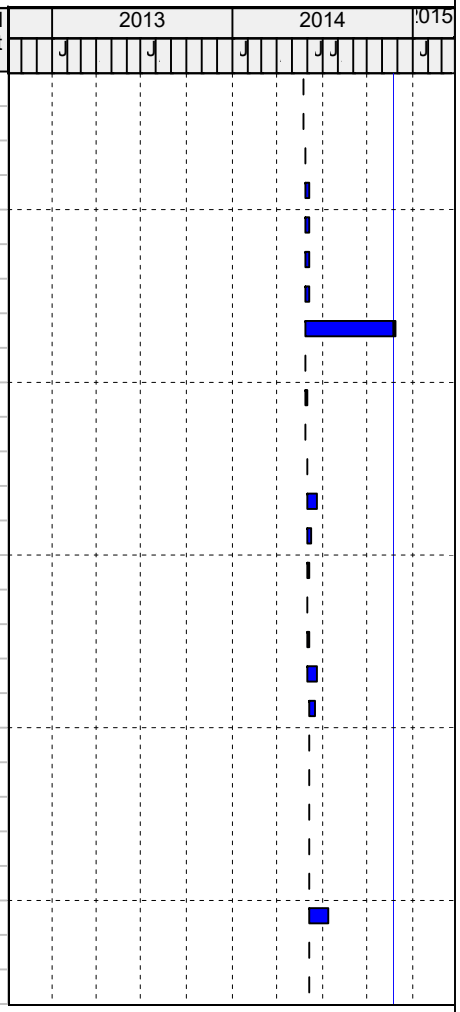



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L09-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 11-Jun-14 A | 12-Jun-14 A | |
| I-3702 | Complete wall framing at Stair/Elevator 5 (LL4) | 2 | 0 | 18-Jun-14 A | 20-Jun-14 A | |
| I-3720 | Fireproof added steel between Stair 1 and Elevator 5 | 5 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| I-3722 | Complete GWB between Stair 1 and Elevator 5 shaft | 10 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| LL1-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 22-Jul-14 A | |
| TC-5912 | Tower Crane pour-backs (LL4 to L3) | 4 | 0 | 19-Jun-14 A | 26-Jun-14 A | |
| LL1-Z2-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL4-6005 | LL4 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| LL3-6005 | LL3 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| L03-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 21-Jun-14 A | 21-Jun-14 A | |
| L06-6040 | Test Heat Pumps - L3, L4, L5 and L6 | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L03-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| L17-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL2-6005 | LL2 - Seismic Head Of Wall Fire Caulk at CMU | 5 | 0 | 24-Jun-14 A | 18-Jul-14 A | |
| I-3704 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL1-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z2-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z3-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 04-Aug-14 A | |
| L1L-6005 | Head of Wall Fire Caulk at CMU (including back of ho | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1K-6005 | Head of Wall Fire Caulk at CMU & Inspection | 2 | 0 | 24-Jun-14 A | 08-Aug-14 A | |
| L03-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L04-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| I-3710 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| I-3712 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| L1K-6018a | Install Kitchen hoods and grease ducts (OFCI) | 10 | 0 | 25-Jun-14 A | 07-Oct-14 A | |

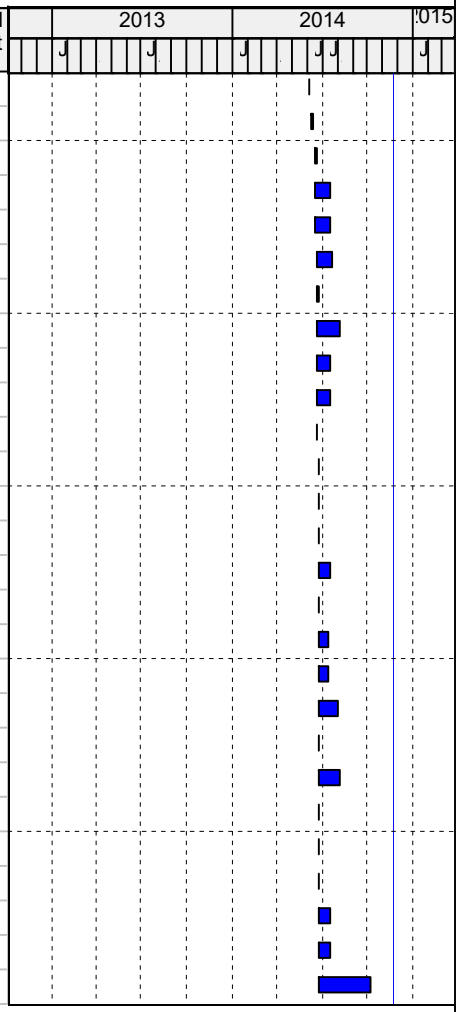


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8604 | L3 Pool - Plumbing R/I | 5 | 0 | 25-Jun-14 A | 10-Nov-14 A | |
| L04-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 26-Jun-14 A | 03-Jul-14 A | |
| L09-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 26-Jun-14 A | 26-Jun-14 A | |
| I-3706 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 26-Jun-14 A | 10-Jul-14 A | |
| L03-8600 | L3 Pool - Framing & HM frames | 5 | 0 | 26-Jun-14 A | 20-Nov-14 A | |
| L05-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L08-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L04-7018 | Electrical Rough-In | 1 | 0 | 27-Jun-14 A | 22-Jul-14 A | |
| L04-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 27-Jun-14 A | 23-Jul-14 A | |
| L03-7020 | HVAC Rough-In | 1 | 0 | 29-Jun-14 A | 15-Jul-14 A | |
| L1RR-8100 | Insulation [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8100 | Insulation [DELETED - included in Ballroom activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8100 | Insulation [DELETED - included in Meeting Rooms ac | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8102 | GWB Hang [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8215 | GWB Tape [DELETED - included in Meeting Rooms a | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8104 | Prime Paint [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8102 | GWB Hang [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8215 | GWB Tape [DELETED - included in Ballroom activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8104 | Prime Paint [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |

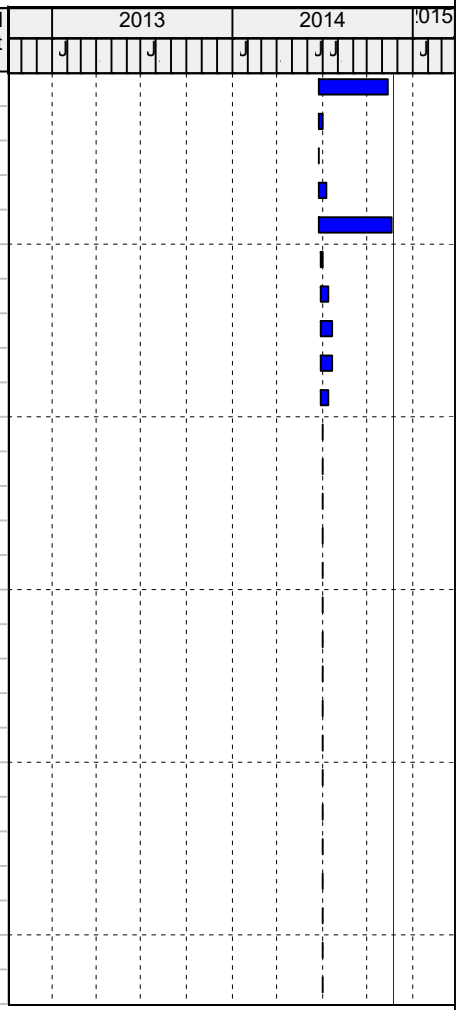



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1RR-8102 | GWB Hang [DELETED - included in Kitchen activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8215 | GWB Tape [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8104 | Prime Paint [DELETED - included in Kitchen activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L03-7018 | Electrical Rough-In | 1 | 0 | 01-Jul-14 A | 14-Jul-14 A | |
| L03-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Jul-14 A | 15-Jul-14 A | |
| L10-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7102 | Install Vertical Heat Pump | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L03-7116 | Frame Walls | 1 | 0 | 02-Jul-14 A | 14-Jul-14 A | |
| L03-7118 | Install HM Door Frame | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L04-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L05-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L07-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L08-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L09-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L10-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L12-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| I-3708 | Complete wall framing at Stair/Elevator 5 (LL3) | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |

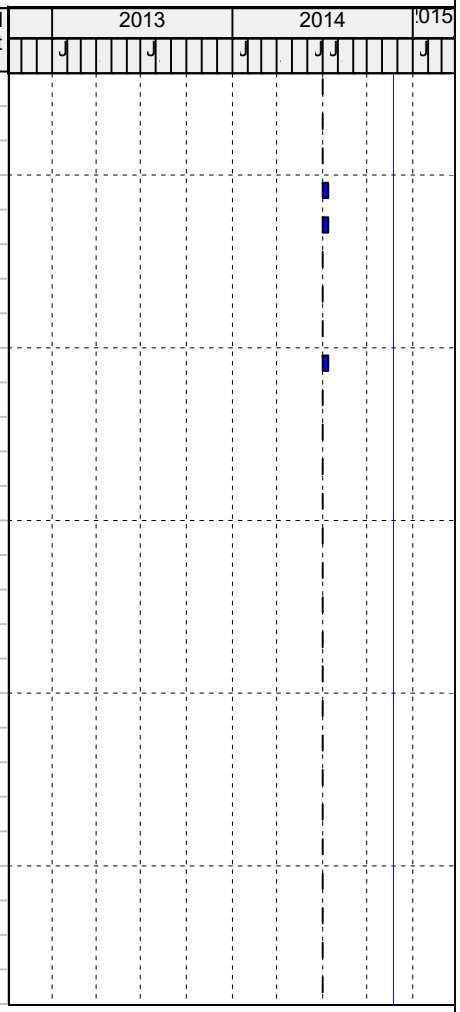



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L11-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 03-Jul-14 A | 07-Jul-14 A | |
| L04-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L05-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L06-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L07-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L08-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L17-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L10-6040 | Test Heat Pumps - L7, L8, L9 and L10 | 3 | 0 | 07-Jul-14 A | 09-Jul-14 A | |
| L10-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L03-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L04-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L05-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L06-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L07-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L08-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L09-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L10-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L12-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |

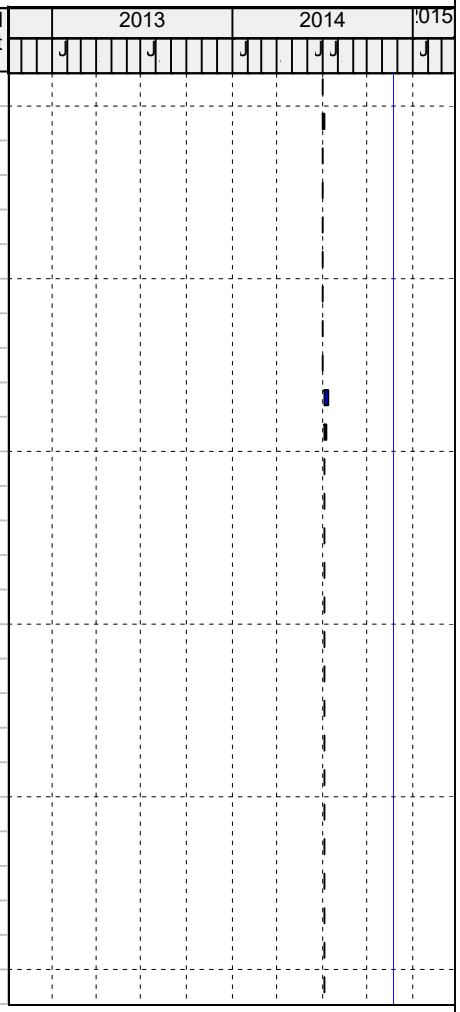



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L11-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Jul-14 A | 29-Jul-14 A | |
| L03-8602 | L3 Pool - Fire Sprinkler R/I | 5 | 0 | 08-Jul-14 A | 22-Jul-14 A | |
| L03-7016 | Install HM door frame | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L11-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L16-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 09-Jul-14 A | |
| L04-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |

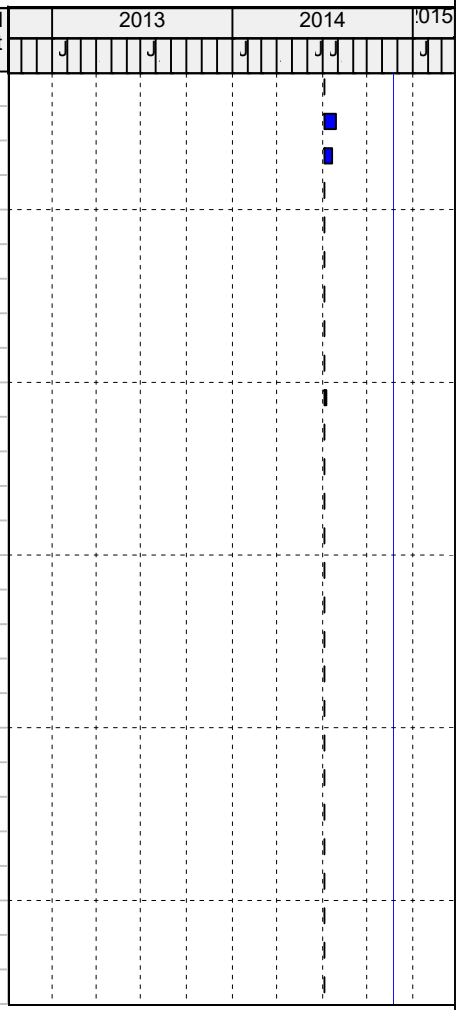



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L12-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| MP-FAB1 | Fabricate and Deliver Bronze Gold Horizontal Panels | 30 | 0 | 09-Jul-14 A | 15-Jul-14 A | |
| L04-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L05-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L06-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L16-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| MP-FAB2 | Fabricate and Deliver Silver Vertical Panels | 45 | 0 | 10-Jul-14 A | 25-Aug-14 A | |
| I-3004 | Issue ASI 38 | 0 | 0 | 11-Jul-14 A | | |
| I-3006 | Release bar area for x-ray examination | 5 | 0 | 11-Jul-14 A | 03-Sep-14 A | |
| L07-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| LL1-Z2-6018a | Complete Mech RI at tower crane opening (LL1) | 4 | 0 | 14-Jul-14 A | 17-Jul-14 A | |
| L08-6223 | Frame Corridor Ceilings | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| SW-2006a | Complete Dry Utilities (Phase 2) | 5 | 0 | 14-Jul-14 A | 24-Jul-14 A | |
| L04-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L04-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L05-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L06-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |

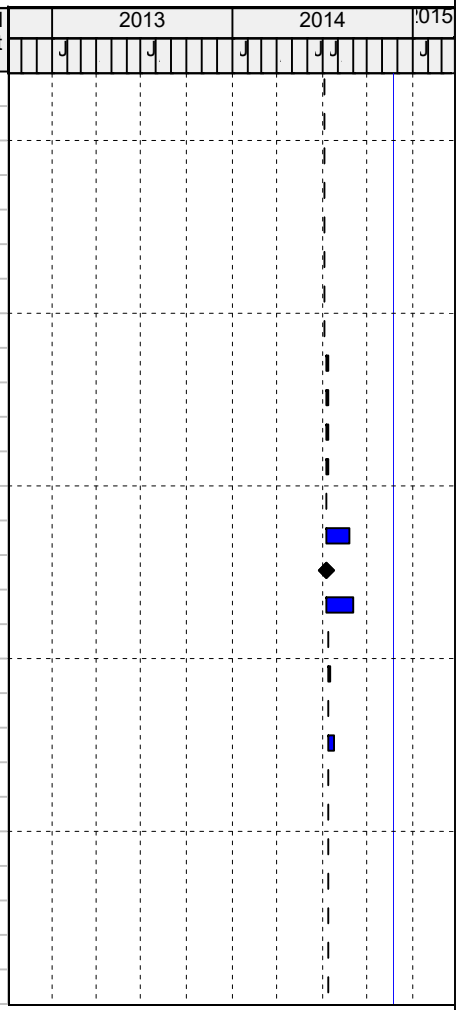



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L04-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L11-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L11-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L12-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L12-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L15-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L15-7102 | Install Vertical Heat Pump | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L1B-6026 | Install operable partition steel | 2 | 0 | 15-Jul-14 A | 08-Aug-14 A | |
| L09-6223 | Frame corridor ceilings | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L03-7120 | Electrical Rough-In | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |

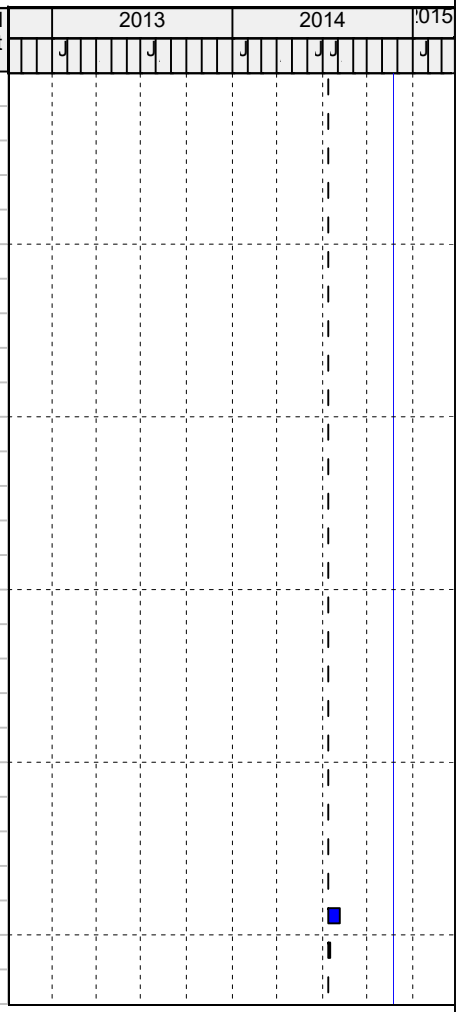



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L07-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L08-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L08-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L09-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L09-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L03-7142 | Install Laundry Chute (All Levels) | 9 | 0 | 15-Jul-14 A | 25-Jul-14 A | |
| LL2-2045 | LL2 - Electrical Room build-out | 15 | 0 | 15-Jul-14 A | 26-Sep-14 A | |
| L03-7122 | HVAC Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L04-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L05-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L06-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L07-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L07-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L08-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L08-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L09-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L09-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |

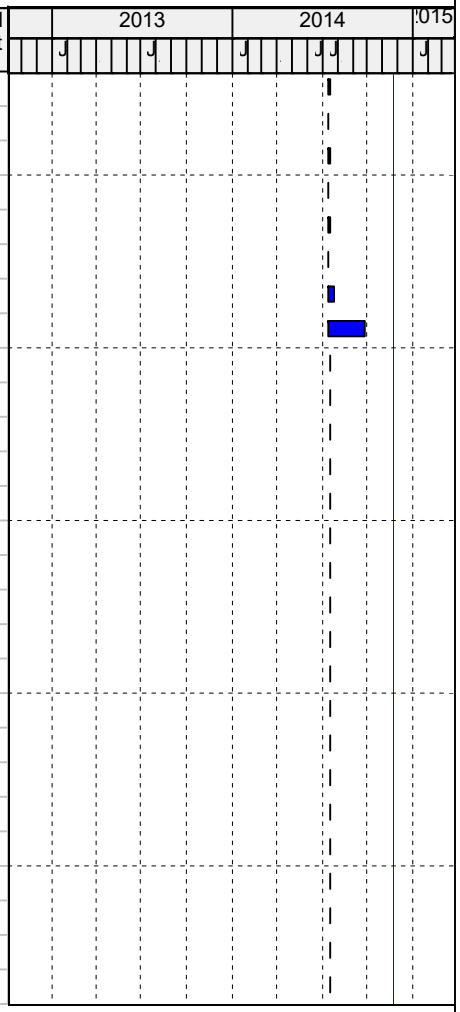



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L11-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L11-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L12-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L12-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L15-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L15-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L16-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L17-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L04-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L04-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L05-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L05-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L06-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L06-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L07-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L08-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L09-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |

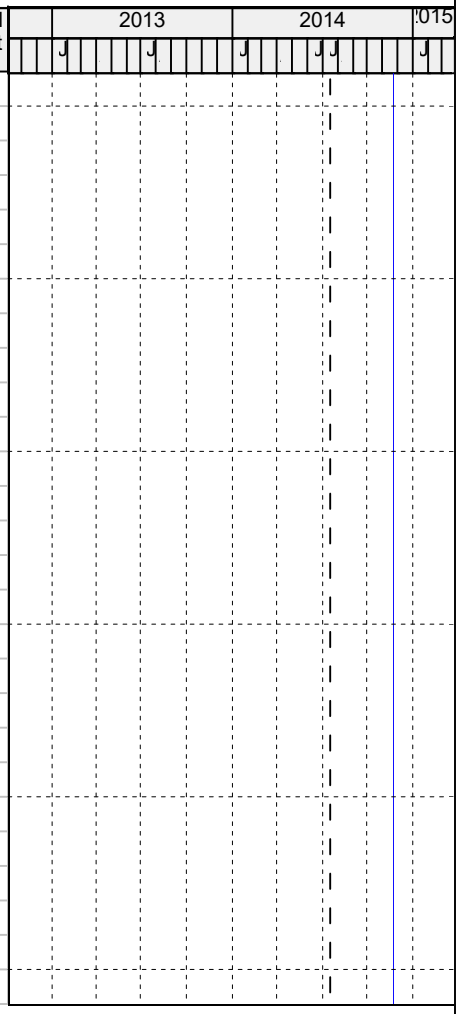



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L11-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L11-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L12-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L12-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L16-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L03-8608 | L3 Pool - Electrical R/I | 5 | 0 | 18-Jul-14 A | 10-Nov-14 A | |
| L03-8610 | L3 Pool - Fire Alarm / Elec Specialties R/I | 5 | 0 | 18-Jul-14 A | 10-Nov-14 A | |
| L15-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L15-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| L17-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L17-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| LL2-2052 | LL2 - Install fuel piping and exhaust duct to Generatc | 8 | 0 | 21-Jul-14 A | 15-Aug-14 A | |
| L04-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L04-7016 | Install HM door frame | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L07-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L08-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L10-7116 | Frame Walls | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L16-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 21-Jul-14 A | 22-Jul-14 A | |
| L16-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |

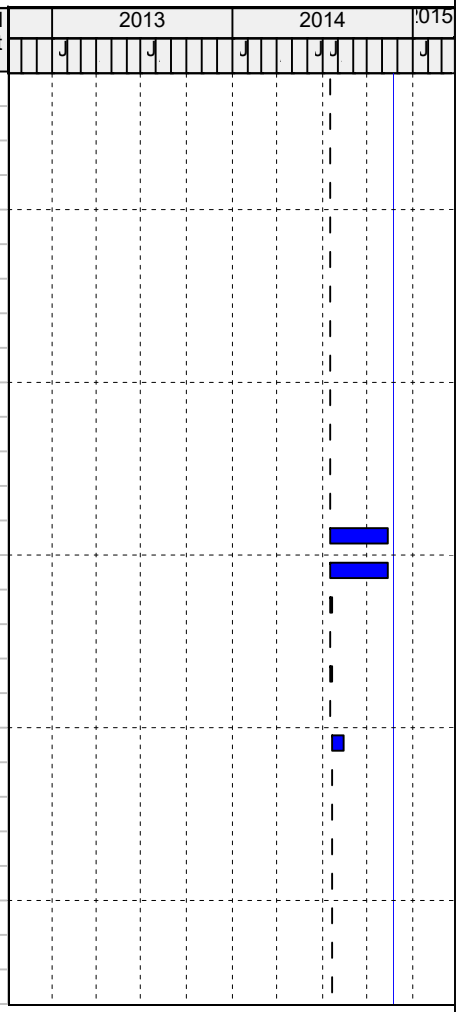



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| MPT-1002 | Tower - Install Elevation 35 (east elevation-south half) | 8 | 0 | 25-Jul-14 A | 04-Aug-14 A | |
| L16-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 25-Jul-14 A | 25-Jul-14 A | |
| L11-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L14-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L15-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L16-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L10-6223 | Frame Corridor Ceilings | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L11-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L15-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L15-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L11-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L14-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L16-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| I-1304 | Prep Kitchen - Additional framing (ASI 30) | 2 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-2302 | Framing "Go Back" work at LL1 for RFI 233 | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| I-2502 | Electrical rework at LL1 for ASIs 7, 9r2, 14, 27 | 4 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| L12-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L1B-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 01-Aug-14 A | 15-Aug-14 A | |
| MPL4-1000 | Upper L4 Ballroom - Install Elevations 1, 2 & 3 (south | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1000 | Tower - Install Elevations 26-27 (west elevation) [DEL | 13 | 0 | 01-Aug-14 A | 01-Aug-14 A | |

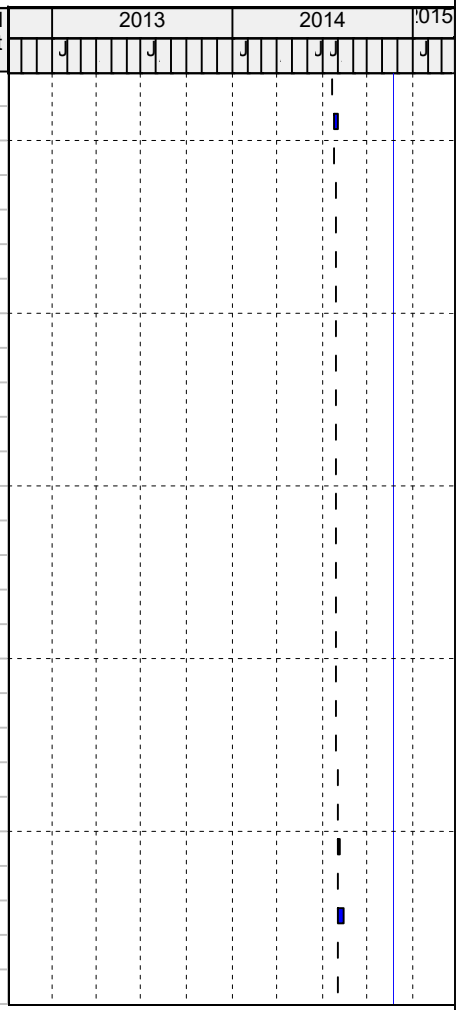



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPP-1002 | Podium - Install Elevations 1 & 2 (west elevation, sou | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPP-1008 | Podium - Install Elevations 7 & 8 (north & east elevati | 9 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1002 | Upper L4 Ballroom - Install Elevation 10 (west elevatic | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1004 | Upper L4 Ballroom - Install Elevation 9 (north elevatio | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1006 | Tower - Install Elevation 40 (east return-east end) [DE | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1010 | Tower - Install Elevations 51 (north elevation) [DELET | 8 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-4004 | East Stitched - Install metal panels [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L11-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L11-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L15-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L14-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L17-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| MPT-1010b | Tower - Install Elevation 45 [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L16-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 04-Aug-14 A | 05-Aug-14 A | |
| L11-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Aug-14 A | 08-Aug-14 A | |
| L04-7020 | HVAC Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |

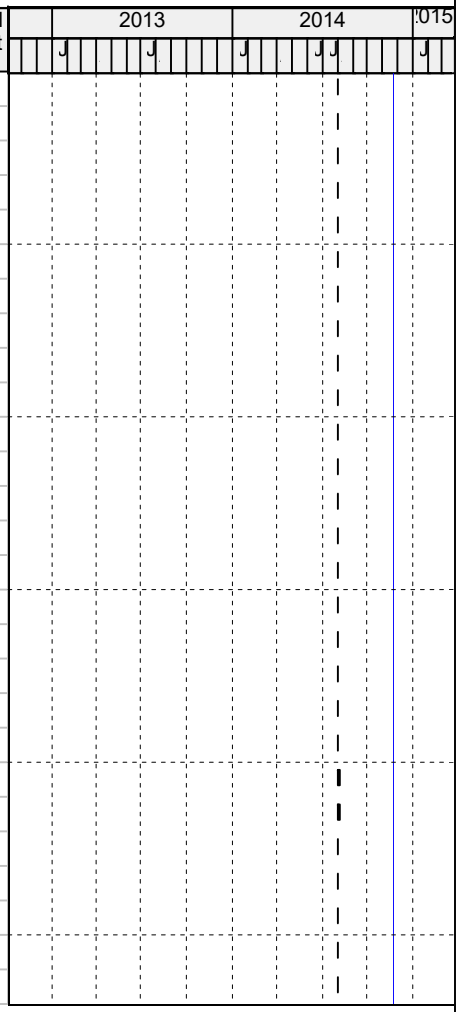



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L14-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L15-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 05-Aug-14 A | 07-Aug-14 A | |
| L05-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L06-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L07-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L08-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L09-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L10-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7018 | Electrical Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L14-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 05-Aug-14 A | 06-Aug-14 A | |
| L14-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| I-4104 | Install added trap primers - LL1 | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L06-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L07-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L08-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L09-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |

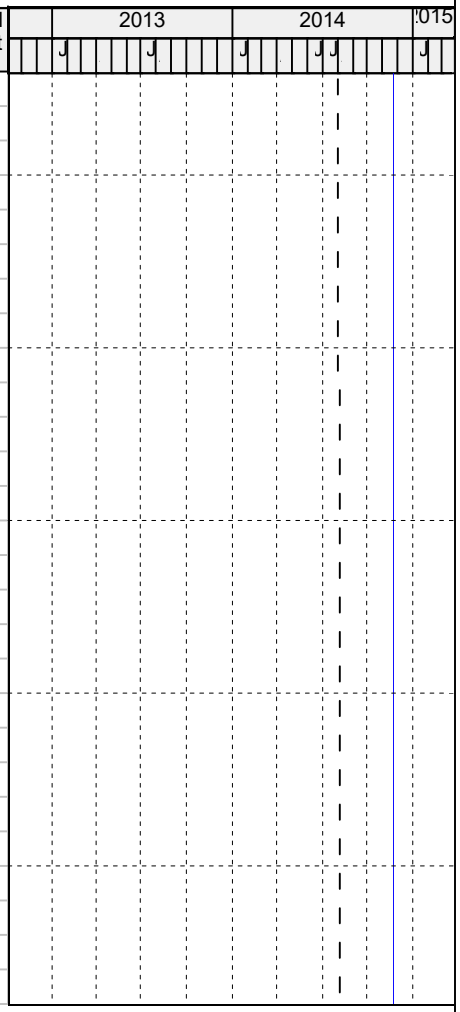



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7020 | HVAC Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L16-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| EL-1220 | Elevator fronts delivered | 0 | 0 | 07-Aug-14 A | | |
| L12-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L12-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-6223 | Frame Corridor Ceilings | 4 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L11-7016 | Install HM door frame | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L12-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L15-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L15-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L16-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L16-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L17-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L17-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-6040 | Test Heat Pumps - L11, L12 and L14 | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| PH-6026 | PH - Insulation/Vapor Barrier/GWB at Exterior Walls | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |

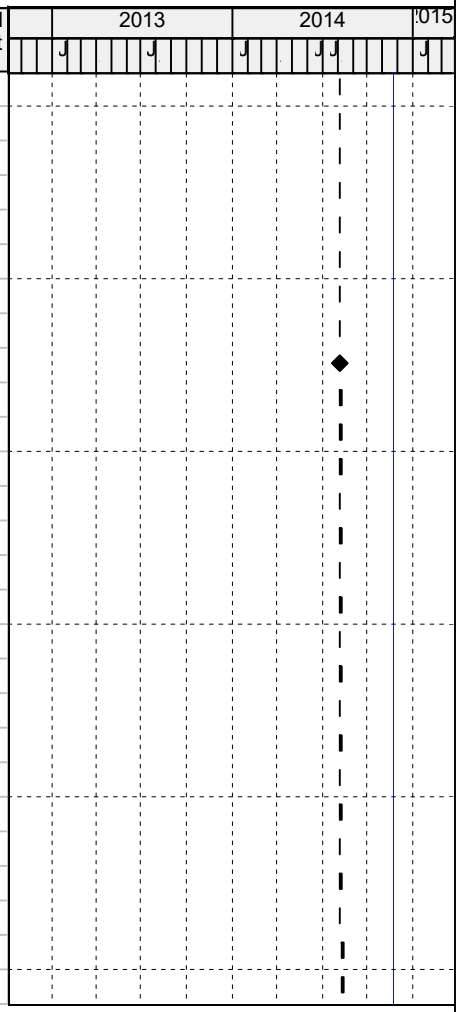



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L11-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-7026 | Inspections for GWB Cover | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 13-Aug-14 A | 13-Aug-14 A | |
| L15-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 14-Aug-14 A | 15-Aug-14 A | |
| LL2E-8108 | LL2 - Set fire pumps and equipment | 5 | 0 | 14-Aug-14 A | 29-Sep-14 A | |
| L10-7028 | GWB Hang/Tape/Finish | 5 | 1 | 14-Aug-14 A | 24-Nov-14 | 37 |
| L12-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L12-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L16-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L1BOH2-6008 | Int Wall Framing & Inspection | 5 | 0 | 14-Aug-14 A | 20-Aug-14 A | |
| I-4106 | Install added trap primers - L1 | 1 | 0 | 15-Aug-14 A | 15-Aug-14 A | |
| L14-6223 | Frame Corridor Ceilings | 4 | 0 | 15-Aug-14 A | 16-Aug-14 A | |
| L03-8136 | Install Counter Subtops | 3 | 0 | 15-Aug-14 A | 18-Aug-14 A | |
| LL2-2054 | LL2 - GWB, Hang 1st Layer at Laundry Room | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| LL2E-8112 | LL2 - Form/Pour Fire Pump Pads/Curbs | 2 | 0 | 16-Aug-14 A | 18-Aug-14 A | |
| LL1-6014Ia | L1 bar redesign - rework plumbing at ceilings | 10 | 5 | 18-Aug-14 A | 02-Dec-14 | 18 |

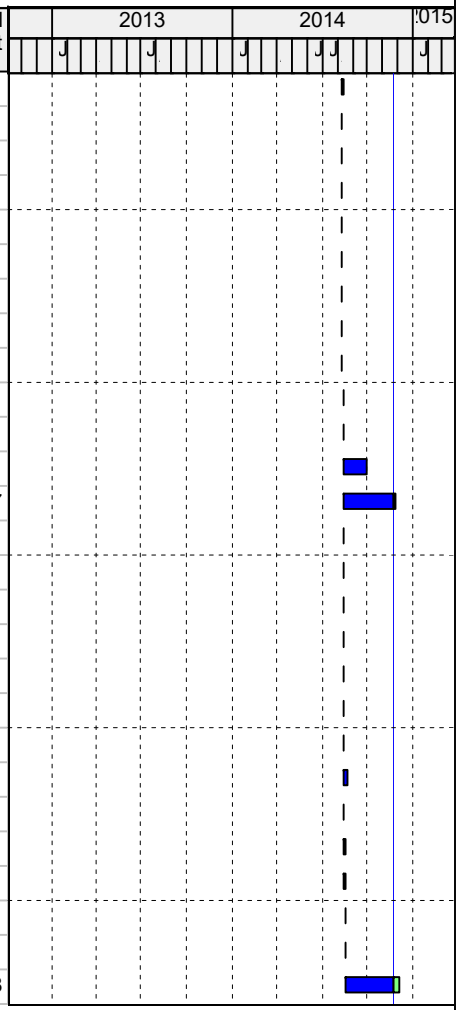



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6223 | Frame Corridor Ceilings | 4 | 0 | 18-Aug-14 A | 21-Aug-14 A | |
| L17-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Aug-14 A | 18-Aug-14 A | |
| L04-8136 | Install Counter Subtops | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-6014Ic | L1 bar redesign - rework electrical at ceilings | 10 | 5 | 18-Aug-14 A | 02-Dec-14 | 23 |
| LL2E-8114 | LL2 - Set Tube Steel at Door | 1 | 0 | 19-Aug-14 A | 19-Aug-14 A | |
| L17-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 20-Aug-14 A | 21-Aug-14 A | |
| L17-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 20-Aug-14 A | 20-Aug-14 A | |
| L05-8136 | Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 26-Aug-14 A | |
| L06-8136 | Bathrooms - Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 13-Oct-14 A | |
| L16-6223 | Frame Corridor Ceilings | 4 | 0 | 21-Aug-14 A | 29-Aug-14 A | |
| L17-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 21-Aug-14 A | 22-Aug-14 A | |
| L17-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 21-Aug-14 A | 21-Aug-14 A | |
| L1BOH2-6016 | Electrical RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6018 | HVAC RI | 4 | 0 | 21-Aug-14 A | 17-Oct-14 A | |
| L15-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7020 | HVAC Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7022 | Fire Sprinkler Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| LL2E-8116 | LL2 - Set Door Jamb | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L04-7028 | GWB Hang/Tape/Finish | 5 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L05-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L05-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L06-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |

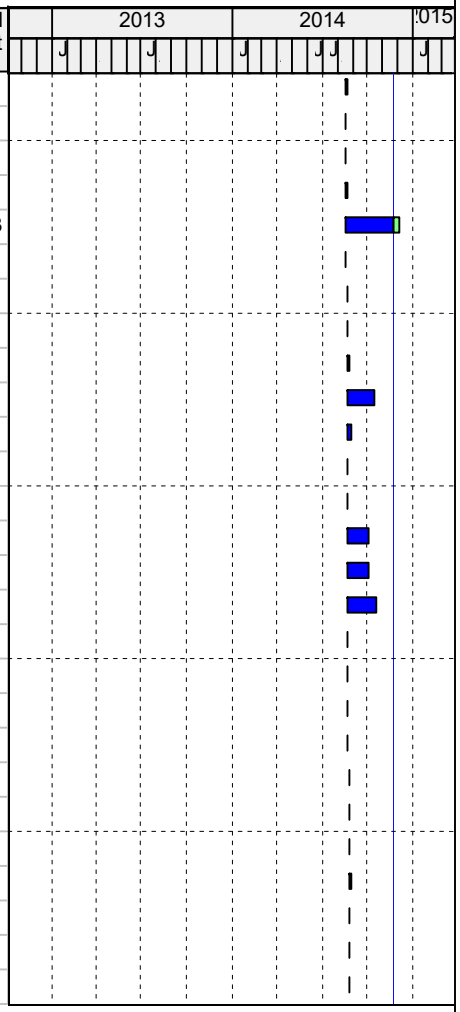



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L03-8123 | Bathroom "Barn Doors" On Site | 0 | 0 | 25-Aug-14 A | | |
| LL3-6026 | LL3 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL2-6026 | LL2 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL1-Z3-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L1BOH2-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |

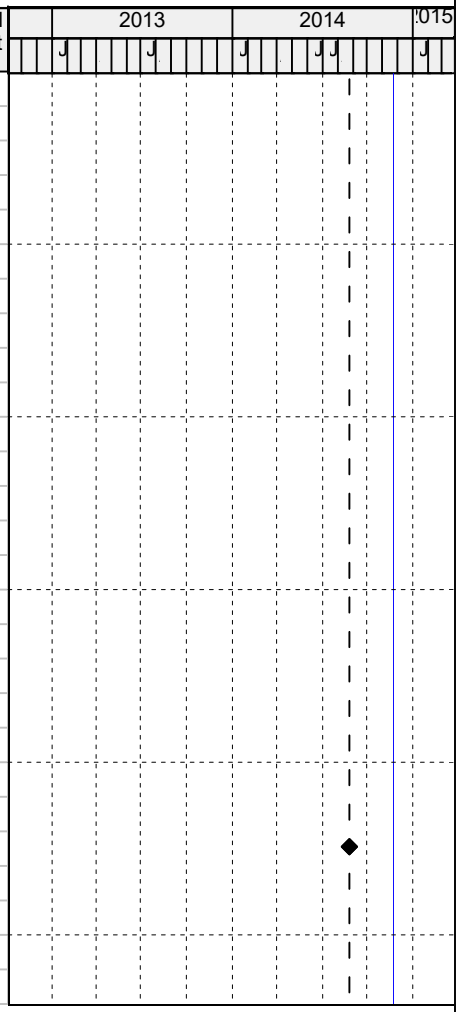



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-6026 | L2 - Set Elevator Fronts (Cars 1-4 | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L03-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L04-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L05-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L06-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L07-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L08-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L09-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L10-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L11-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L12-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L14-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L15-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L16-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L17-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| MPT-1008 | Tower - Install E/W Wing, N. Side West Half (Elev 50, | 7 | 0 | 26-Aug-14 A | 03-Oct-14 A | |
| L06-6005 | CMU Fire Caulk/Clips | 2 | 1 | 26-Aug-14 A | 24-Nov-14 | 48 |
| L07-6005 | CMU Fire Caulk/Clips | 2 | 1 | 26-Aug-14 A | 24-Nov-14 | 48 |
| L08-6005 | CMU Fire Caulk/Clips | 2 | 1 | 26-Aug-14 A | 24-Nov-14 | 48 |
| L05-7026 | Inspections for GWB Cover | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L05-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L11-7028 | GWB Hang/Tape/Finish | 5 | 1 | 26-Aug-14 A | 24-Nov-14 | 38 |
| L12-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L14-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L03-8105a | Painting - Split Door Jambs | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L09-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 24-Nov-14 | 48 |
| L10-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 24-Nov-14 | 48 |

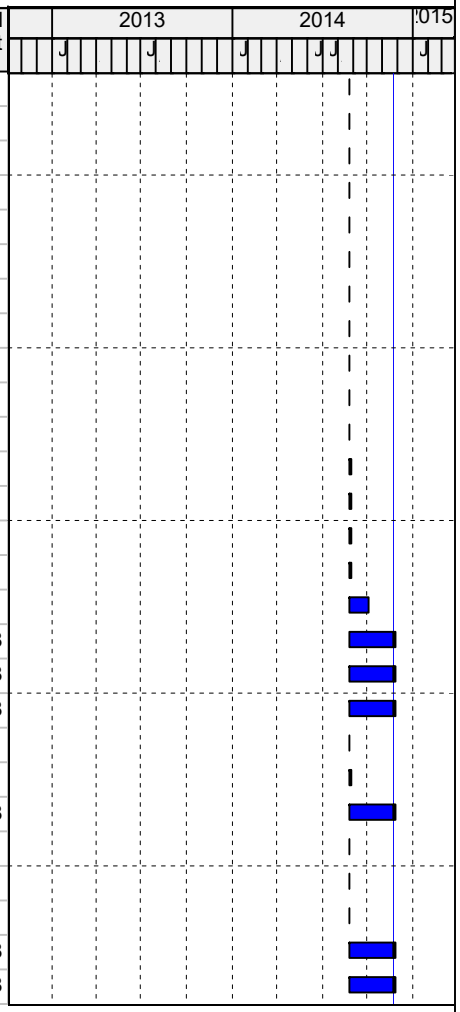



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 25-Nov-14 | 48 |
| L12-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 25-Nov-14 | 48 |
| L14-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 25-Nov-14 | 48 |
| L15-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 25-Nov-14 | 48 |
| L16-6005 | CMU Fire Caulk/Clips | 2 | 1 | 27-Aug-14 A | 25-Nov-14 | 48 |
| L05-8201 | Install ACT Grid @ Corridors | 2 | 0 | 27-Aug-14 A | 28-Aug-14 A | |
| L16-7022 | Fire Sprinkler Rough-In | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L04-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L06-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| EP-5110a | L1 - Install Steel at Revolving Door Opening | 3 | 0 | 27-Aug-14 A | 29-Aug-14 A | |
| L05-8105a | Painting - Split Door Jambs | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| I-4102 | Install added trap primers - LL2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4108 | Install added trap primers - L2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4110 | Install added trap primers - L3 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4112 | Install added trap primers - Roof PH | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| L03-8124d | Flooring On Site and Acclimated | 2 | 0 | 29-Aug-14 A | 01-Sep-14 A | |
| L02-5102 | L2 - Storefront Frames | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| L04-6005 | CMU Fire Caulk/Clips | 2 | 1 | 02-Sep-14 A | 24-Nov-14 | 48 |
| L05-6005 | CMU Fire Caulk/Clips | 2 | 1 | 02-Sep-14 A | 24-Nov-14 | 48 |
| L17-6005 | CMU Fire Caulk/Clips | 2 | 1 | 02-Sep-14 A | 25-Nov-14 | 48 |
| L03-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L12-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L14-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L07-8136 | Install Counter Subtops | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| LL1-Z3-FCC10 | FCC - Set Jamb | 1 | 0 | 02-Sep-14 A | 03-Sep-14 A | |
| MPT-1004 | Tower - Install E/W Wing, S. Side w/o Windows (Elev | 10 | 0 | 03-Sep-14 A | 17-Oct-14 A | |
| L03-7028 | GWB Hang/Tape/Finish | 5 | 1 | 03-Sep-14 A | 24-Nov-14 | 30 |

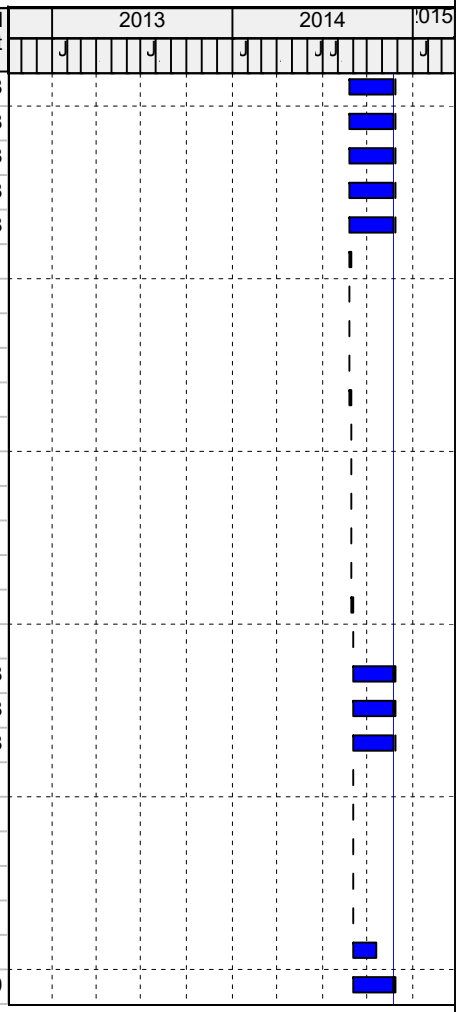



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7028 | GWB Hang/Tape/Finish | 5 | 1 | 03-Sep-14 A | 24-Nov-14 | 39 |
| L03-8126a | Doors & Hardware On Site | 0 | 0 | 03-Sep-14 A | | |
| LL1-Z3-FCC12 | FCC - Sheetrock Outside Wall | 1 | 0 | 03-Sep-14 A | 03-Sep-14 A | |
| L16-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| L17-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Sep-14 A | 11-Sep-14 A | |
| L02-5104b | L2 - Install Storefront Temporary Enclosures | 1 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| LL1-Z3-FCC14 | FCC - Verify Fire Caulk OK & Inspect Room OK to 2n | 1 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| I-3008 | Coordinate and perform x-ray examination | 7 | 0 | 04-Sep-14 A | 12-Sep-14 A | |
| L02-5104a | L2 - Measure/Fabricate Storefront Glazing | 15 | 0 | 05-Sep-14 A | 18-Sep-14 A | |
| LL1-Z3-FCC16 | FCC - GWB, Hang 2nd Layer | 2 | 0 | 05-Sep-14 A | 08-Sep-14 A | |
| L03-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L15-7018 | Electrical Rough-In | 1 | 0 | 08-Sep-14 A | 08-Sep-14 A | |
| EL-1228 | Construct/Approve elevator lobby framing mockup (L | 3 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| LL2E-8118 | LL2 - Frame Infill, Install Densglass & Inspect at Fire I | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L06-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L08-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L15-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7018 | Electrical Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L3-5104a | L3 - Measure/Fabricate Storefront Glazing | 15 | 0 | 09-Sep-14 A | 30-Sep-14 A | |
| L03-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 23-Sep-14 A | |
| L03-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L04-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L06-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| L08-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |

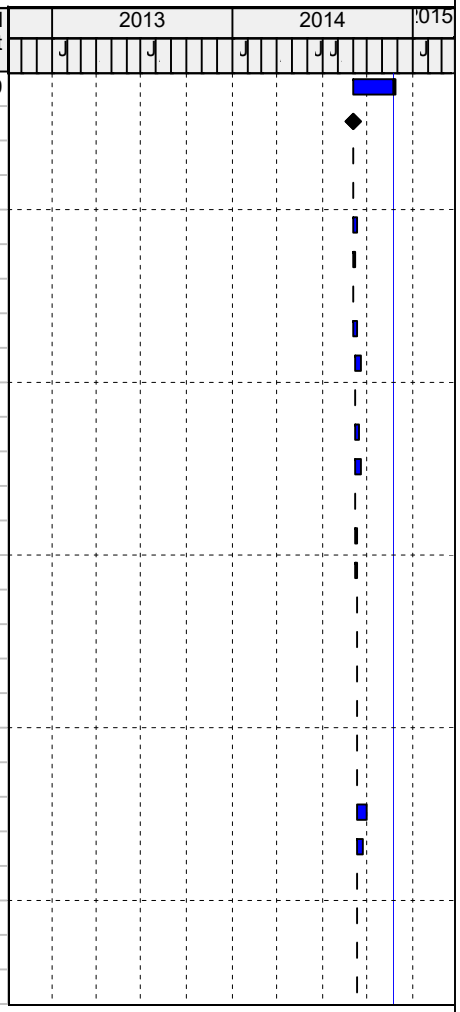



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L06-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L06-7028 | GWB Hang/Tape/Finish | 5 | 1 | 10-Sep-14 A | 24-Nov-14 | 33 |
| L08-7028 | GWB Hang/Tape/Finish | 5 | 1 | 10-Sep-14 A | 24-Nov-14 | 35 |
| L15-7026 | Inspections for GWB Cover | 1 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| LL2E-8120 | LL2 - Insulation, Vapor Barrier & Inspect at Fire Pump | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L08-8395 | Framing at Elevator Lobby | 4 | 0 | 11-Sep-14 A | 17-Sep-14 A | |
| L15-7028 | GWB Hang/Tape/Finish | 5 | 1 | 11-Sep-14 A | 24-Nov-14 | 41 |
| L08-8136 | Install Counter Subtops | 3 | 0 | 11-Sep-14 A | 16-Sep-14 A | |
| L02-6025 | L2 - Framing Go-Back Work (left out for mechanical e | 4 | 0 | 11-Sep-14 A | 02-Oct-14 A | |
| L1-5104a | L1 - Measure/Fabricate Storefront Glazing | 15 | 0 | 12-Sep-14 A | 18-Sep-14 A | |
| L1B-8102c | Finish framing and MEP at Main Ballroom East Wall ( | 10 | 0 | 12-Sep-14 A | 02-Oct-14 A | |
| L09-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L10-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L11-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L12-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L16-7026 | Inspections for GWB Cover | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| MPT-1014 | Tower - Install E/W Wing, N. Side, E. Half (Elev 46-49 | 8 | 0 | 15-Sep-14 A | 28-Oct-14 A | |
| LL2-6032 | LL2 - Complete Framing (Including Elevator Lobby) | 4 | 0 | 15-Sep-14 A | 18-Sep-14 A | |
| L1-5104b | L1 - Install Storefront Temporary Enclosures | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| LL1-Z3-FCC18 | FCC - Install Temp Door | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| LL2-2058a | LL2 - GWB Hang 1st Layer | 5 | 0 | 15-Sep-14 A | 19-Sep-14 A | |
| LL2-2064 | LL2 - Generator Room - Finish Exhaust Piping | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| I-3010 | Prepare proposal for MEP relocations | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| L16-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L07-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |

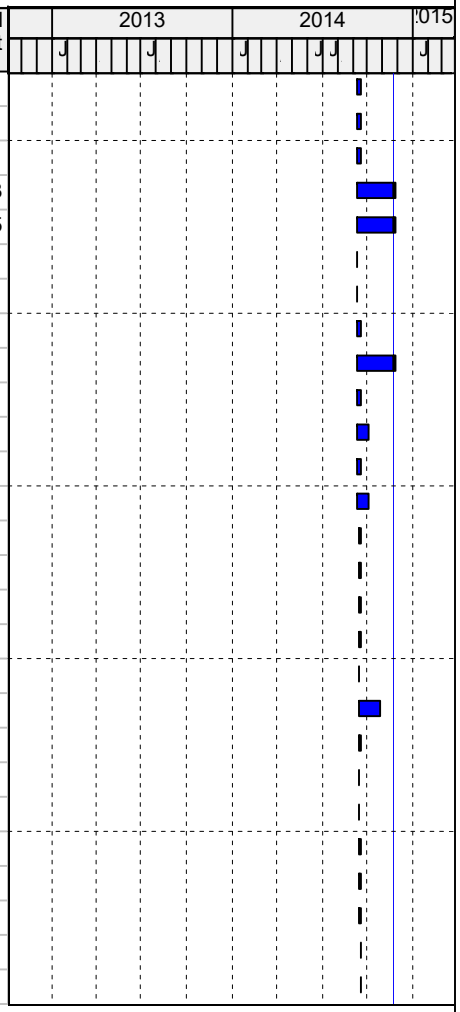



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L10-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L14-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L15-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L03-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| L16-7028 | GWB Hang/Tape/Finish | 5 | 1 | 16-Sep-14 A | 24-Nov-14 | 42 |
| L17-7018 | Electrical Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L09-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L10-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| LL3-6028 | LL3 - Frame Elevator Lobby | 2 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| LL4-6026 | LL4 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| I-3012 | Owner approve proposal for MEP relocations | 3 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| L11-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L12-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L14-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L15-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L04-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L17-7026 | Inspections for GWB Cover | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L17-7116 | Frame Walls | 4 | 0 | 17-Sep-14 A | 29-Sep-14 A | |
| LL2-2066 | LL2 - Generator Room - Finish Fuel Piping | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L16-8395 | Framing at Elevator Lobby | 4 | 0 | 18-Sep-14 A | 26-Sep-14 A | |
| L02-5104 | L2 - Storefront Glazing | 2 | 0 | 18-Sep-14 A | 22-Sep-14 A | |
| L17-7028 | GWB Hang/Tape/Finish | 5 | 1 | 18-Sep-14 A | 24-Nov-14 | 43 |
| LL4-6028 | LL4 - Frame Elevator Lobby | 2 | 0 | 18-Sep-14 A | 02-Oct-14 A | |
| MPT-1010a | Tower - Install E/W Wing, West End (Elev 52,53) | 8 | 0 | 18-Sep-14 A | 10-Oct-14 A | |
| LL2-2068 | LL2 - Generator Room - Electrical Finishes | 3 | 0 | 19-Sep-14 A | 30-Sep-14 A | |

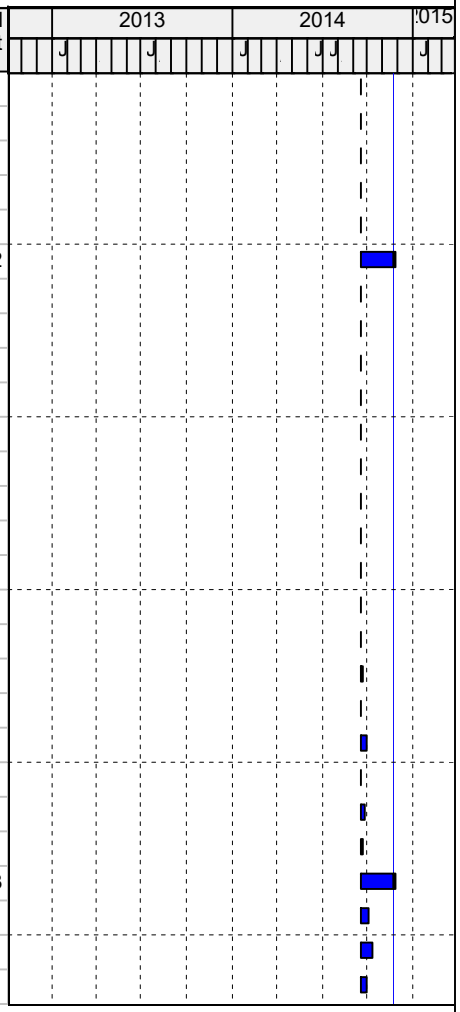



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L09-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L04-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L05-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L03-8140 | Countertops On Site | 0 | 0 | 22-Sep-14 A | | |
| L03-8129a | Shower Doors On Site | 0 | 0 | 22-Sep-14 A | | |
| LL1-Z3-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L1BOH2-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2-2048a | LL2 - Move in Laundry Room Ironer | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2E-8122 | LL2 - Hang GWB at Fire Pump Room | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-FCC20 | FCC - Rough-In and Install Panels | 25 | 0 | 22-Sep-14 A | 21-Nov-14 A | |
| I-3014 | Core drill for MEP relocations | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L05-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L07-7028 | GWB Hang/Tape/Finish | 5 | 1 | 23-Sep-14 A | 24-Nov-14 | 34 |
| L09-7028 | GWB Hang/Tape/Finish | 5 | 1 | 23-Sep-14 A | 24-Nov-14 | 36 |
| L14-7028 | GWB Hang/Tape/Finish | 5 | 1 | 23-Sep-14 A | 24-Nov-14 | 40 |
| L04-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L05-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L06-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L07-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L04-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L06-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L04-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |

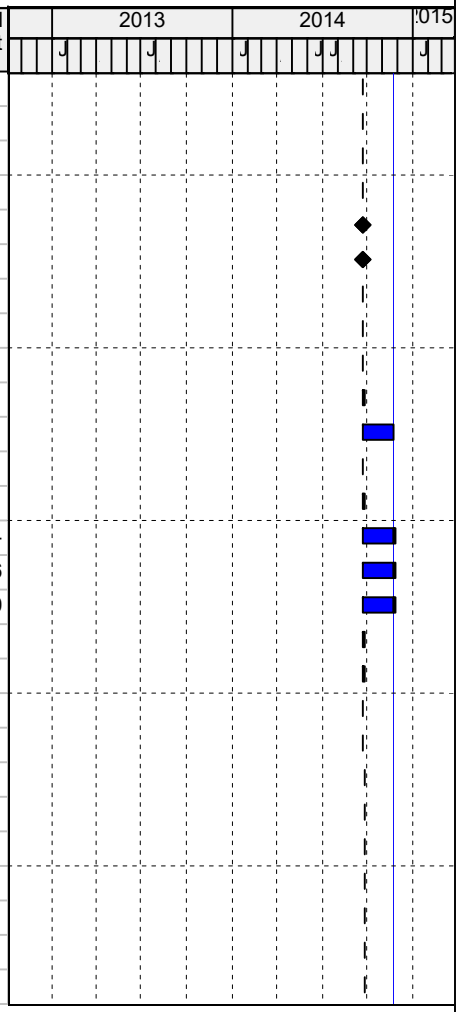



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-7122 | HVAC Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| LL2-2058 | LL2 - Tape/Finish Laundry Room | 3 | 0 | 24-Sep-14 A | 26-Sep-14 A | |
| L08-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L17-8395 | Framing at Elevator Lobby | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L05-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L06-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L07-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L08-7120 | Electrical Rough-In | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| LL2E-8124 | LL2 - Temp-In Louver Opening at Fire Pump Room | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L1-5104c | L1 - Install Storefront at Main Entry Facade | 5 | 0 | 25-Sep-14 A | 10-Oct-14 A | |
| L16-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L08-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L10-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L16-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L17-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L17-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L09-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L11-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |

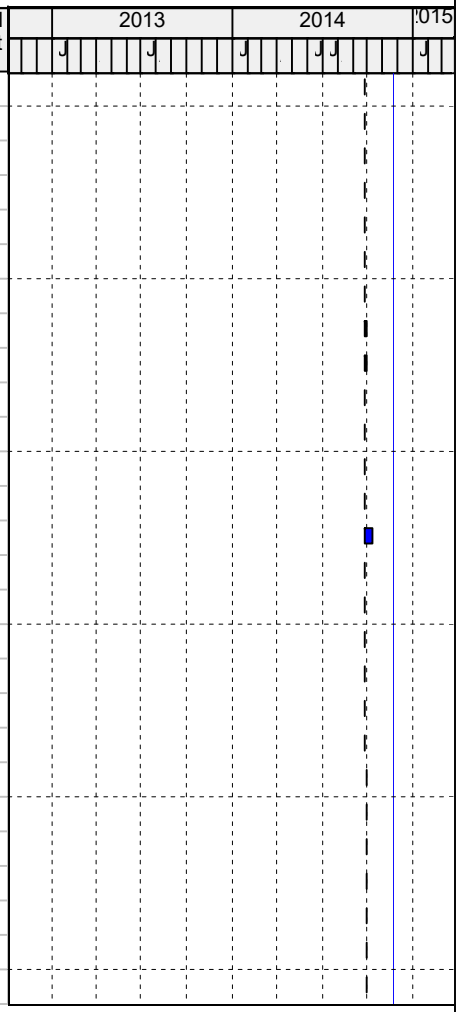



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L14-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L15-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L17-7118 | Install HM Door Frame | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| LL3-6030 | LL3 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL4-6030 | LL4 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL2-6034 | LL2 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L1BOH2-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L02-6030 | L2 - Framing at Elevator Lobby & North Half | 4 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| MPT-1022 | Tower - Caulking, west | 8 | 0 | 29-Sep-14 A | 03-Nov-14 A | |
| PH-6015 | PH - Set Boilers and Pumps | 12 | 0 | 29-Sep-14 A | 15-Oct-14 A | |
| L11-8204 | Bathrooms - Vinyl Wall Coverings | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L10-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L17-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L11-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L12-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L07-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 30-Sep-14 A | 08-Oct-14 A | |
| L11-8201 | Install ACT Grid @ Corridors | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L09-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L09-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L11-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L12-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L14-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L15-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| LL2-2072 | Generator - Complete generator and annunciator cor | 5 | 0 | 30-Sep-14 A | 21-Oct-14 A | |

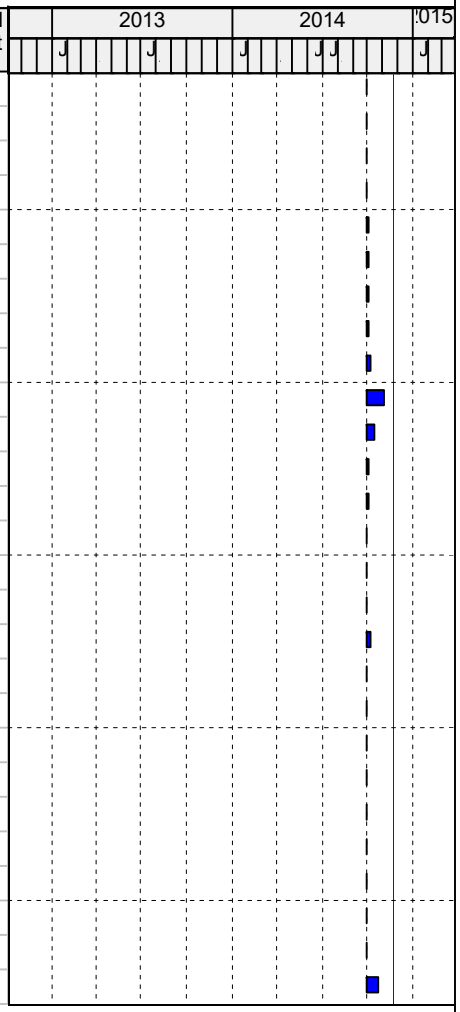



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6040 | Test Heat Pumps - L16 and L17 | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L17-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L14-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L03-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |

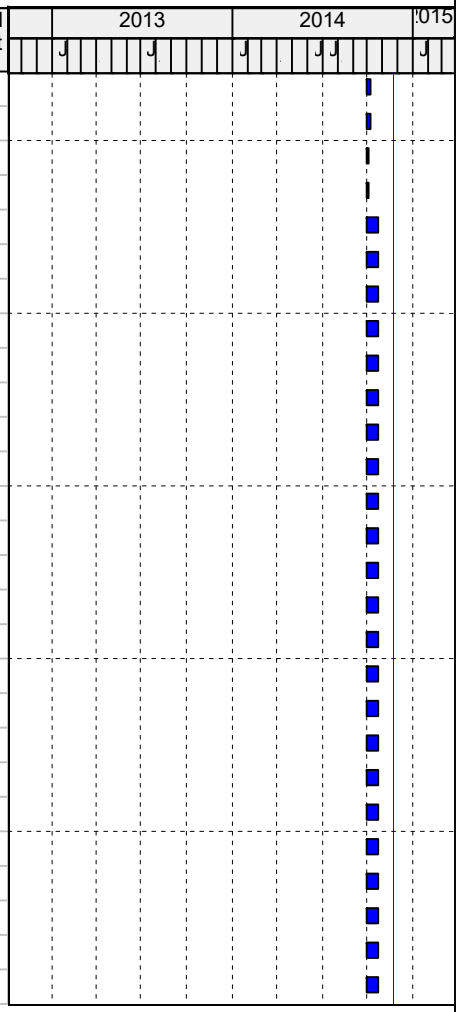



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L11-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L12-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L12-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L14-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L16-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L17-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L09-8136 | Install Counter Subtops | 3 | 0 | 01-Oct-14 A | 03-Oct-14 A | |
| L02-6032 | L2 - Electrical RI at Elevator Lobby & North Half | 5 | 0 | 01-Oct-14 A | 08-Oct-14 A | |
| SW-2306 | Prep, grind and overlay at 11th Ave, 3rd Place & 2nd | 5 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 01-Oct-14 A | 25-Nov-14 | 35 |
| L16-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |

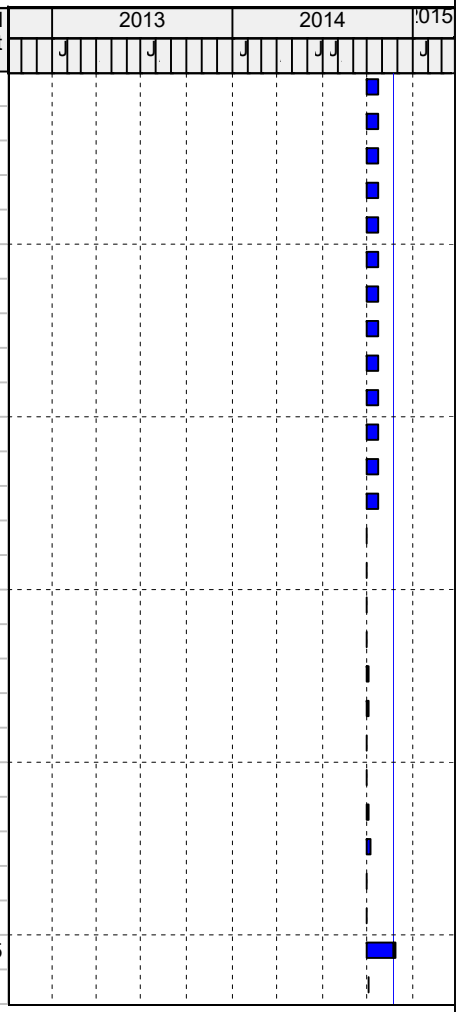



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L14-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L15-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1BOH2-8130 | Inspections For Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L02-6024a | L2 - Inspections - South Half | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L06-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| L17-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| LL2-2074 | Generator - Install fuel fill | 2 | 0 | 03-Oct-14 A | 06-Oct-14 A | |
| L07-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| MPT-1020 | Tower - Install E/W Wing, East End (Elev 41,44) | 5 | 0 | 06-Oct-14 A | 18-Oct-14 A | |
| LL1-8102a | GWB Hang/Tape (Ceilings) | 10 | 0 | 06-Oct-14 A | 18-Nov-14 A | |
| L1BOH2C-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6014 | Complete Plumbing RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6016 | Complete Electrical RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6018 | Complete HVAC RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L03-8200a | New murals on site (date estimated) | 0 | 0 | 06-Oct-14 A | | |
| SW-2100 | Zone 1 - Survey curb & site lighting | 2 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 06-Oct-14 A | 06-Oct-14 A | |
| L1BOH2-8100 | Insulation | 4 | 0 | 07-Oct-14 A | 13-Oct-14 A | |
| L17-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L12-8201 | Install ACT Grid @ Corridors | 2 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| L10-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 07-Oct-14 A | 20-Oct-14 A | |
| LL1-Z3-6032 | GWB Hang/Tape at Elevator Lobby | 5 | 2 | 07-Oct-14 A | 25-Nov-14 | 32 |

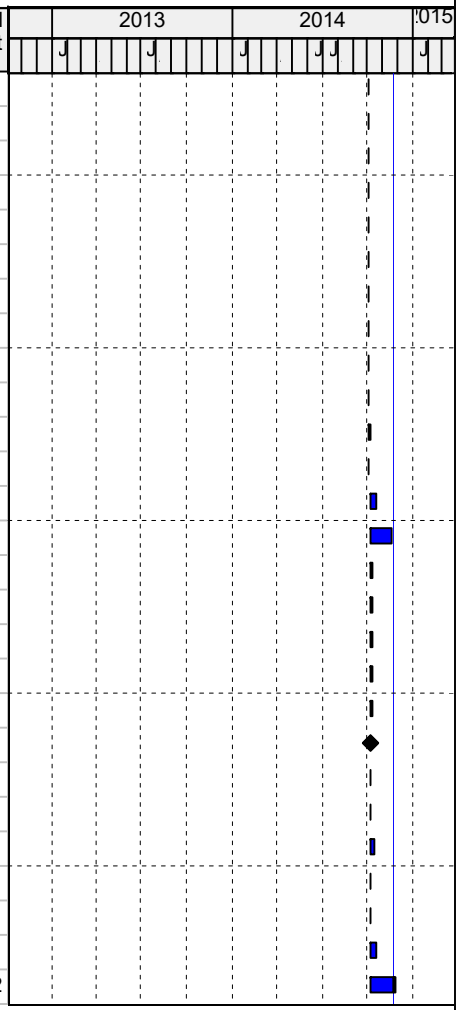



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8216x | Vinyl Wall Coverings - Install Murals | 2 | 1 | 07-Oct-14 A | 24-Nov-14 | 36 |
| L1B-8102b | GWB Hang (Walls) & Inspection - Exterior Wall at Cor | 3 | 0 | 07-Oct-14 A | 09-Oct-14 A | |
| RF-4048 | Tower Roof - Install davit arms | 3 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| LL2-2076 | Generator - Install fuel fill mechanical piping | 4 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L12-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L09-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L03-8633 | Pool - Install waterproofing & test | 3 | 0 | 08-Oct-14 A | 17-Oct-14 A | |
| L03-8130 | Install Door Hardware | 3 | 0 | 08-Oct-14 A | 28-Oct-14 A | |
| L10-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L02-8102a | L2 - GWB Hang / Tape / Finish - South Half | 7 | 0 | 09-Oct-14 A | 27-Oct-14 A | |
| SW-2102 | Zone 1 - Vacate SE corner | 2 | 0 | 09-Oct-14 A | 11-Oct-14 A | |
| SW-2106 | Zone 1 - Sawcut and remove asphalt | 4 | 0 | 09-Oct-14 A | 14-Oct-14 A | |
| L11-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 09-Oct-14 A | |
| SW-2200 | Zone 2 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |
| SW-2300 | Zone 3 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |
| SW-2108 | Zone 1 - Install east footing drain | 4 | 0 | 10-Oct-14 A | 20-Oct-14 A | |
| L04-8130 | Install Door Hardware | 3 | 0 | 10-Oct-14 A | 29-Oct-14 A | |
| ML-5962 | Man/Material Lifts - Remove Roof Lift Stop | 0 | 0 | | 11-Oct-14 A | |
| I-1102 | Additional work at new L17 guest rooms | 5 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| LL2-2046 | LL2 - Generator Room - Misc. Finishes | 3 | 0 | 13-Oct-14 A | 21-Nov-14 A | |
| RF-4008 | Tower Roof - Install corrugated metal panels | 5 | 0 | 13-Oct-14 A | 03-Nov-14 A | |
| MPT-1018b | Tower - Roof cornice frame & sheath | 6 | 0 | 13-Oct-14 A | 24-Oct-14 A | |
| L02-8100a | L2 - Insulation - South Half | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| SW-2112 | Zone 1 - Grade for curb and gutter | 3 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| SW-2202 | Zone 2 - Install site lighting | 5 | 1 | 13-Oct-14 A | 24-Nov-14 | 64 |
| SW-2204 | Zone 2 - Repave utility trenches | 4 | 0 | 13-Oct-14 A | 22-Oct-14 A | |
| L12-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 13-Oct-14 A | |

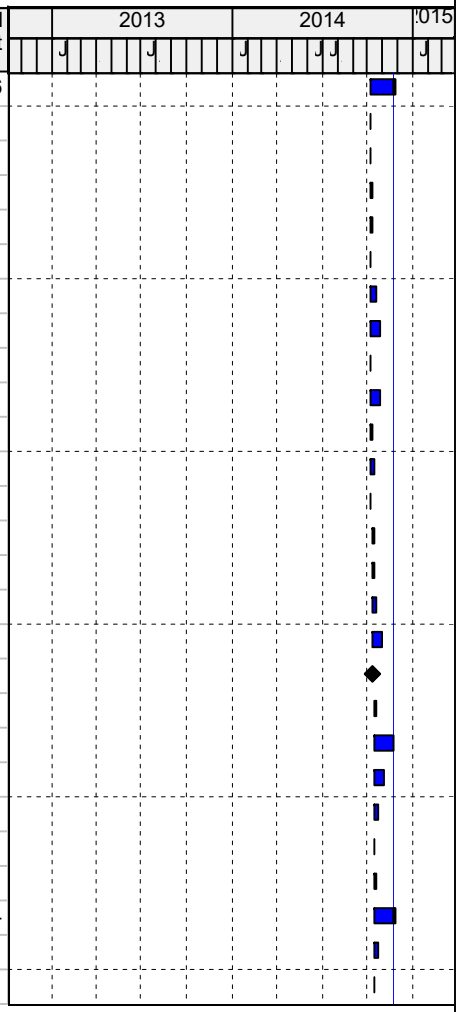



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2302 | Zone 3 - Grade for curb and gutter | 2 | 2 | 14-Oct-14 A | 04-Dec-14 | 70 |
| L14-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 14-Oct-14 A | 16-Oct-14 A | |
| L05-8130 | Install Door Hardware | 3 | 0 | 14-Oct-14 A | 03-Nov-14 A | |
| L14-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 14-Oct-14 A | |
| L16-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L15-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 15-Oct-14 A | 17-Oct-14 A | |
| L15-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 15-Oct-14 A | |
| SW-2206 | Zone 2 - Grade for curb and gutter | 2 | 0 | 16-Oct-14 A | 20-Oct-14 A | |
| MPP-1000 | Podium - Install W/S/N Elevations (Elev 1-5, 6,9-19,2 | 10 | 5 | 20-Oct-14 A | 02-Dec-14 | 68 |
| L06-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 20-Oct-14 A | 23-Oct-14 A | |
| LL2-8106a | LL2 - Pinned Insulation | 4 | 1 | 20-Oct-14 A | 24-Nov-14 | 51 |
| L1B-8102d | GWB Hang (Walls) & Inspection - Main Ballroom East | 1 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| SW-2114 | Zone 1 - FRP curb and gutter | 2 | 0 | 20-Oct-14 A | 14-Nov-14 A | |
| RF-4044 | Ballroom Roof - Install metal coping | 3 | 0 | 20-Oct-14 A | 13-Nov-14 A | |
| L08-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 21-Oct-14 A | 23-Oct-14 A | |
| MPT-1018 | Tower - Install Roof Penthouse (Elev 36b,37,38.39) | 5 | 3 | 21-Oct-14 A | 26-Nov-14 | 53 |
| L11-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2208 | Zone 2 - FRP curb and gutter | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2304 | Zone 3 - FRP curb and gutter | 3 | 2 | 21-Oct-14 A | 05-Dec-14 | 70 |
| L15-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L06-8130 | Install Door Hardware | 3 | 0 | 21-Oct-14 A | 03-Nov-14 A | |
| L03-8634 | Pool - Install reinforcing steel & inspect | 5 | 0 | 22-Oct-14 A | 30-Oct-14 A | |

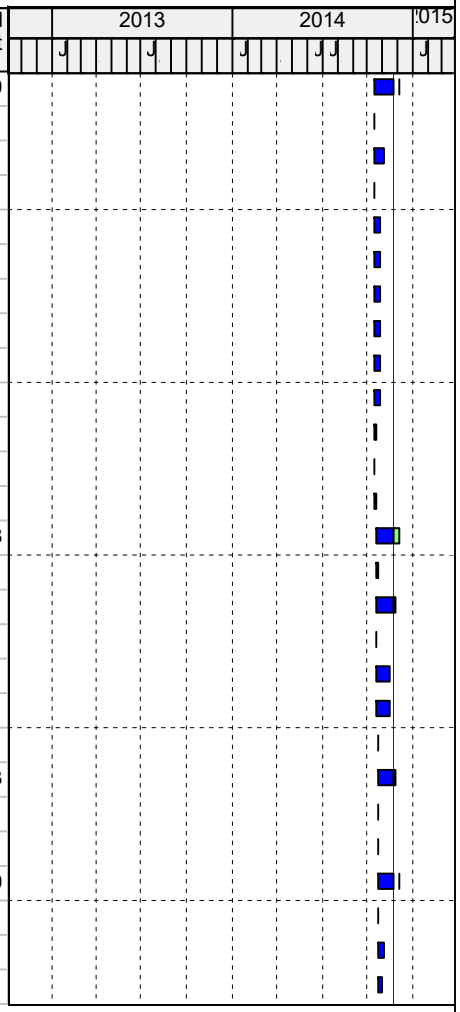



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPT-1016 | Tower - Install N/S Wing, S. End W. of Manlift (Elev 2 | 5 | 2 | 22-Oct-14 A | 25-Nov-14 | 51 |
| SW-2116 | Zone 1 - Fine grade for sidewalk | 3 | 0 | 22-Oct-14 A | 11-Nov-14 A | |
| LL4-8106 | LL4 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| LL3-8106 | LL3 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L14-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L08-8130 | Install Door Hardware | 3 | 0 | 22-Oct-14 A | 04-Nov-14 A | |
| L07-8130 | Install Door Hardware | 3 | 0 | 22-Oct-14 A | 03-Nov-14 A | |
| L03-8606 | L3 Pool - HVAC R/I | 3 | 0 | 23-Oct-14 A | 27-Oct-14 A | |
| L09-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 23-Oct-14 A | 03-Nov-14 A | |
| L12-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| LL2-2078 | Generator - Install fuel fill control wiring | 2 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| RF-4050 | Roof at Manlift - Erect steel | 1 | 0 | 24-Oct-14 A | 24-Oct-14 A | |
| CO-7204 | Cx - Gas Service established | 0 | 0 | | 24-Oct-14 A | |
| L1BOH2-8102 | GWB Hang (Walls) | 4 | 0 | 27-Oct-14 A | 07-Nov-14 A | |
| L04-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 27-Oct-14 A | 12-Nov-14 A | |
| RF-4052 | Roof at Manlift - Framing/sheathing/air barrier (inspec | 4 | 0 | 27-Oct-14 A | 30-Oct-14 A | |
| LL2-2080 | Generator - Complete generator accessories (battery) | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| LL2-2082 | Generator - Cx fuel fill | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| L09-8130 | Install Door Hardware | 3 | 0 | 28-Oct-14 A | 04-Nov-14 A | |
| CO-7158 | Generator - Interim electrical inspection | 1 | 0 | 29-Oct-14 A | 29-Oct-14 A | |
| LL2-2070 | LL2 - Generator Room - Generator Ready for Startup | 0 | 0 | | 30-Oct-14 A | |
| LL2-2084 | Generator - Initial fuel fill | 1 | 0 | 30-Oct-14 A | 30-Oct-14 A | |
| CO-7200 | Cx - Penthouse Mechanical Installation Complete | 0 | 0 | | 30-Oct-14 A | |
| EL-6028 | Elev 6 - RFI-761: Response, pricing, complete work (r | 20 | 18 | 30-Oct-14 A | 19-Dec-14 | 26 |
| L03-8636 | Pool - Shotcrete | 1 | 0 | 31-Oct-14 A | 31-Oct-14 A | |
| RF-4054 | Roof at Manlift - Final mechanical installations | 4 | 0 | 31-Oct-14 A | 05-Nov-14 A | |
| RF-4056 | Roof at Manlift - Final electrical connections | 2 | 0 | 31-Oct-14 A | 05-Nov-14 A | |

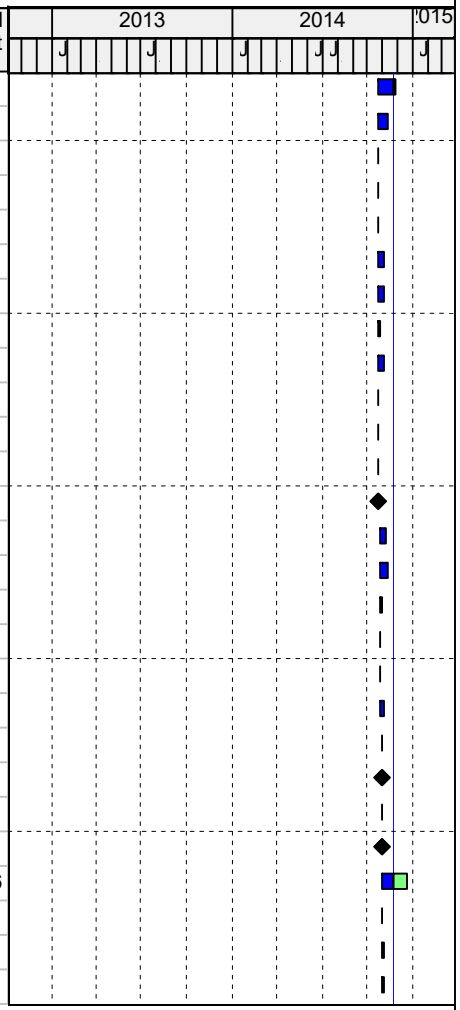


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8404 | GWB Hang/Tape Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 14-Nov-14 A | |
| L04-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 14-Nov-14 A | |
| L05-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 17-Nov-14 A | |
| L06-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 17-Nov-14 A | |
| L03-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L04-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L05-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L06-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L07-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L08-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L09-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L10-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L11-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L12-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L14-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L15-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L16-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L17-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L14-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 03-Nov-14 A | 06-Nov-14 A | |
| RF-4064 | Pool Green Roof - Install sheet metal capping | 3 | 1 | 03-Nov-14 A | 02-Dec-14 | 55 |
| MPT-1024 | Tower - Caulking, east | 20 | 5 | 03-Nov-14 A | 02-Dec-14 | 47 |
| CO-7206 | Cx - Purge/Prove Gas-Fed Equipment and Feeder Li | 7 | 0 | 03-Nov-14 A | 09-Nov-14 A | |
| L07-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 17-Nov-14 A | |
| L08-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L09-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L10-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| RF-4046 | Tower Roof - Install sheet metal capping | 3 | 1 | 04-Nov-14 A | 24-Nov-14 | 55 |

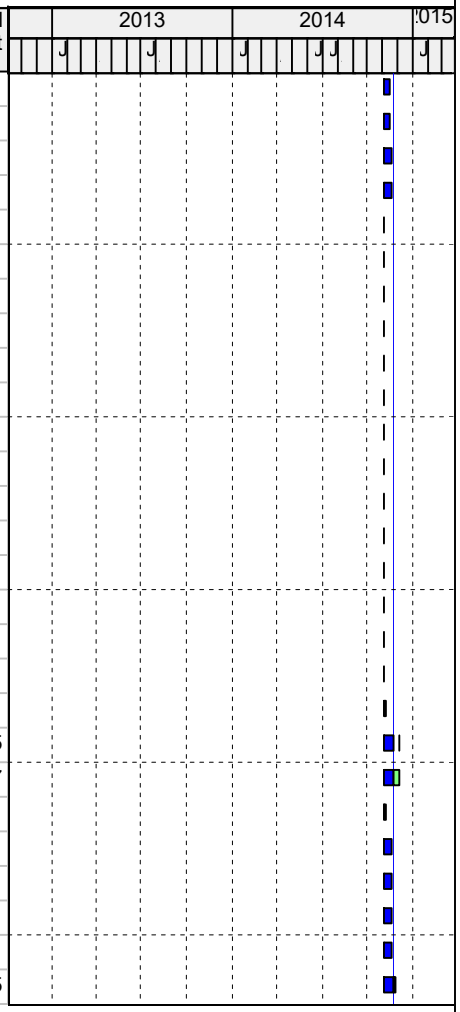


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L11-8216 | Vinyl Wall Coverings - Install Murals | 2 | 1 | 04-Nov-14 A | 04-Dec-14 | 39 |
| L11-8130 | Install Door Hardware | 3 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L10-8130 | Install Door Hardware | 3 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L11-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 18-Nov-14 A | |
| L12-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 19-Nov-14 A | |
| L14-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 19-Nov-14 A | |
| MPP-1010 | Podium - Install East Elevation (Elev 5 & 7) | 7 | 2 | 05-Nov-14 A | 25-Nov-14 | 53 |
| CO-7162 | Generator - Load bank testing | 1 | 0 | 05-Nov-14 A | 05-Nov-14 A | |
| CO-7202 | Cx - Electrical Internal Bus & LL2-L17 Bus Duct Energ | 0 | 0 | | 05-Nov-14 A | |
| CO-7202a | Cx - Energize normal power distribution | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| L15-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 19-Nov-14 A | |
| L16-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 20-Nov-14 A | |
| L17-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 20-Nov-14 A | |
| RF-4058 | Roof at Manlift - Install roofing | 2 | 0 | 06-Nov-14 A | 07-Nov-14 A | |
| CO-7164 | Generator - Final electrical inspection | 1 | 0 | 06-Nov-14 A | 06-Nov-14 A | |
| L15-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 07-Nov-14 A | 12-Nov-14 A | |
| L03-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L03-7130 | GWB Hang/Tape/Finish | 5 | 3 | 10-Nov-14 A | 26-Nov-14 | 29 |
| L04-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L04-7130 | GWB Hang/Tape/Finish | 5 | 3 | 10-Nov-14 A | 26-Nov-14 | 29 |
| L05-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L05-7130 | GWB Hang/Tape/Finish | 5 | 3 | 10-Nov-14 A | 26-Nov-14 | 31 |
| L06-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L06-7130 | GWB Hang/Tape/Finish | 5 | 3 | 10-Nov-14 A | 26-Nov-14 | 33 |
| L07-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L07-7130 | GWB Hang/Tape/Finish | 5 | 3 | 10-Nov-14 A | 26-Nov-14 | 35 |

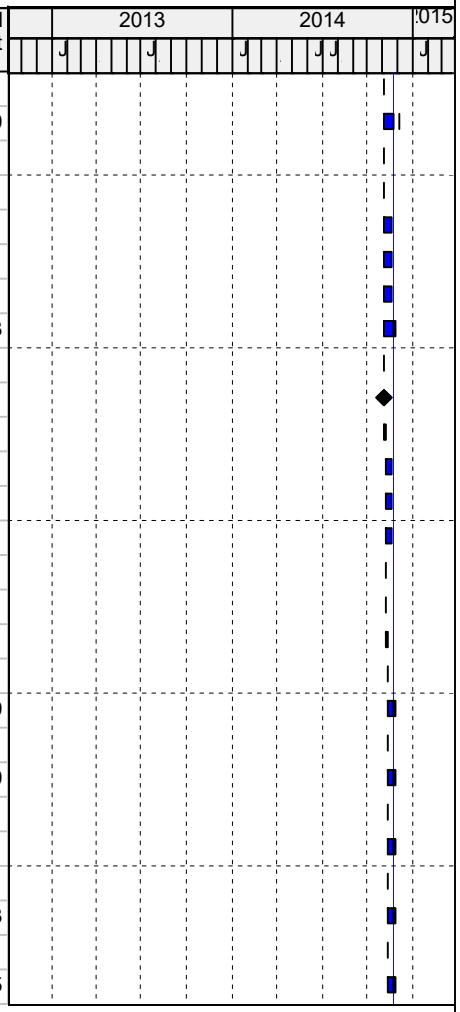



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L08-7130 | GWB Hang/Tape/Finish | 5 | 3 | 10-Nov-14 A | 26-Nov-14 | 37 |
| L09-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L09-7130 | GWB Hang/Tape/Finish | 5 | 3 | 10-Nov-14 A | 26-Nov-14 | 39 |
| L10-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L10-7130 | GWB Hang/Tape/Finish | 5 | 3 | 10-Nov-14 A | 26-Nov-14 | 41 |
| L11-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L11-7130 | GWB Hang/Tape/Finish | 5 | 3 | 10-Nov-14 A | 26-Nov-14 | 40 |
| L12-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L12-7130 | GWB Hang/Tape/Finish | 5 | 3 | 10-Nov-14 A | 26-Nov-14 | 40 |
| L14-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L14-7130 | GWB Hang/Tape/Finish | 5 | 3 | 10-Nov-14 A | 26-Nov-14 | 40 |
| L15-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L15-7130 | GWB Hang/Tape/Finish | 5 | 3 | 10-Nov-14 A | 26-Nov-14 | 41 |
| L16-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L16-7130 | GWB Hang/Tape/Finish | 5 | 3 | 10-Nov-14 A | 26-Nov-14 | 41 |
| L17-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L17-7130 | GWB Hang/Tape/Finish | 5 | 3 | 10-Nov-14 A | 26-Nov-14 | 41 |
| L05-8216 | Vinyl Wall Coverings - Install Murals | 2 | 1 | 10-Nov-14 A | 25-Nov-14 | 37 |
| L06-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 10-Nov-14 A | 11-Nov-14 A | |
| MPT-1032 | Tower - Install sign backing NW (Elev 51,52) | 4 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L12-8130 | Install Door Hardware | 3 | 0 | 10-Nov-14 A | 12-Nov-14 A | |
| EL-1230 | Elev 1&2 - Complete hoistway ventilation | 13 | 3 | 10-Nov-14 A | 26-Nov-14 | 47 |
| EL-1232 | Elev 1&2 - Wire & startup AC split units | 13 | 3 | 10-Nov-14 A | 26-Nov-14 | 75 |
| EL-1234 | Elev 1&2 - Install EMR doors, hardware & labeling | 13 | 3 | 10-Nov-14 A | 26-Nov-14 | 47 |
| EL-3428 | Elev 3&4 - Complete hoistway ventilation | 13 | 3 | 10-Nov-14 A | 26-Nov-14 | 47 |
| EL-3430 | Elev 3&4 - Wire & startup AC split units | 13 | 3 | 10-Nov-14 A | 26-Nov-14 | 47 |

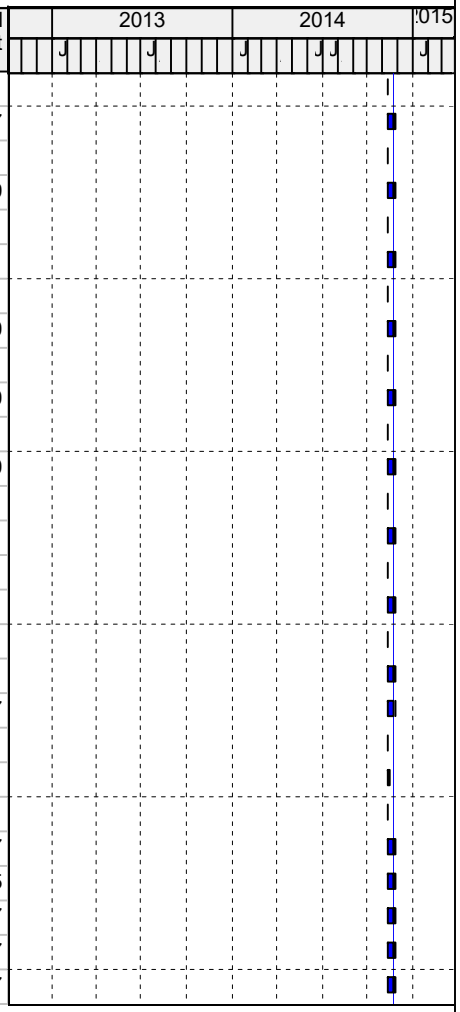



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-3432 | Elev 3&4 - Install EMR doors, hardware & labeling | 13 | 3 | 10-Nov-14 A | 26-Nov-14 | 47 |
| EL-6030 | Elev 6 - Complete fire-rated assemblies at hoistway, l | 13 | 3 | 10-Nov-14 A | 26-Nov-14 | 27 |
| L07-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 11-Nov-14 A | 12-Nov-14 A | |
| SW-2118 | Zone 1 - FRP sidewalk | 3 | 1 | 11-Nov-14 A | 03-Dec-14 | 62 |
| L16-8106 | Paint - Accent Walls | 2 | 0 | 11-Nov-14 A | 12-Nov-14 A | |
| L14-8130 | Install Door Hardware | 3 | 0 | 11-Nov-14 A | 13-Nov-14 A | |
| L03-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 12-Nov-14 A | 18-Nov-14 A | |
| SW-2104 | Zone 1 - Install lighting conduit at SE corner | 2 | 0 | 12-Nov-14 A | 14-Nov-14 A | |
| L16-8111 | Paint - Door Jambs | 2 | 0 | 12-Nov-14 A | 13-Nov-14 A | |
| EL-6010i | Elev 6 - Pit Slab Correction (form/pour/strip/clean) | 10 | 3 | 12-Nov-14 A | 26-Nov-14 | 27 |
| SW-2024 | Zone 4 - FRP Porte Cochere planter & bench | 6 | 1 | 12-Nov-14 A | 24-Nov-14 | 60 |
| L08-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| SW-2109 | Zone 1 - Install irrigation sleeves | 2 | 0 | 13-Nov-14 A | 14-Nov-14 A | |
| MPT-1026 | Tower - Caulking, north | 20 | 18 | 13-Nov-14 A | 19-Dec-14 | 47 |
| L16-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| L15-8130 | Install Door Hardware | 3 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| L04-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 14-Nov-14 A | 19-Nov-14 A | |
| SW-2203 | Zone 2 - Install irrigation sleeves | 2 | 1 | 14-Nov-14 A | 24-Nov-14 | 62 |
| SW-2316 | Zone 3 - Demolish manlift shack and base | 5 | 0 | 17-Nov-14 A | 20-Nov-14 A | |
| I-1610 | Enclosure at manlift - Install exterior wall panels & ins | 5 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| L04-8140 | Install window sills | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| L03-8140x | Install window sills | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| L16-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| SW-2014 | Porte Cochere - Electrical rough-in | 5 | 1 | 17-Nov-14 A | 24-Nov-14 | 43 |
| LL1-Z3-FCC24 | FCC - Complete ceiling and access panels (RFI 734) | 13 | 8 | 17-Nov-14 A | 05-Dec-14 | 35 |
| LL1-Z3-FCC26 | FCC - Program FACP | 13 | 8 | 17-Nov-14 A | 05-Dec-14 | 35 |
| L06-8140 | Install window sills | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |

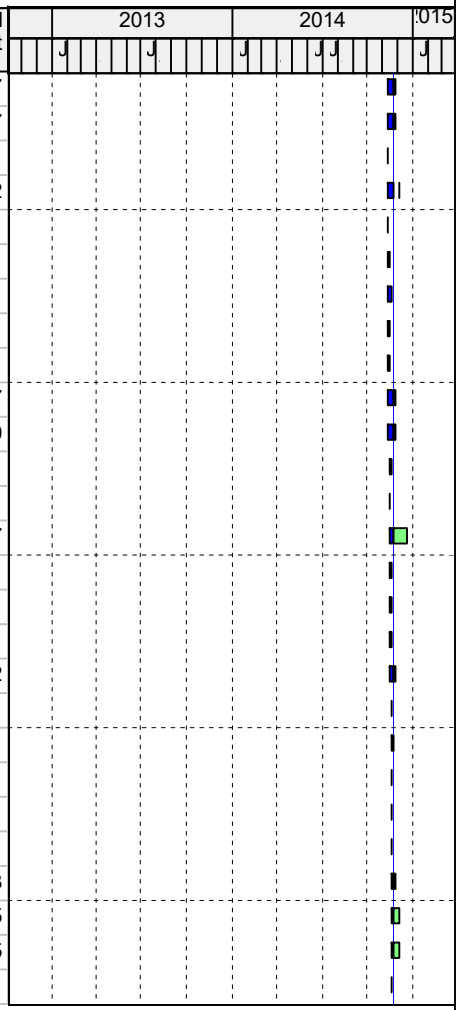



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8140 | Install window sills | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L05-8129 | Bathrooms - Install Shower Doors | 4 | 1 | 19-Nov-14 A | 24-Nov-14 | 49 |
| L16-8130 | Install Door Hardware | 3 | 2 | 19-Nov-14 A | 15-Dec-14 | 37 |
| L08-8140 | Install window sills | 2 | 0 | 19-Nov-14 A | 19-Nov-14 A | |
| L07-8140 | Install window sills | 2 | 0 | 19-Nov-14 A | 19-Nov-14 A | |
| L10-8140 | Install window sills | 2 | 0 | 20-Nov-14 A | 20-Nov-14 A | |
| L09-8140 | Install window sills | 2 | 0 | 20-Nov-14 A | 20-Nov-14 A | |
| L03-8616 | L3 Pool - GWB above ceiling | 2 | 0 | 21-Nov-14 A | 22-Nov-14 A | |
| L1BOH2-8215 | GWB Tape (Walls) | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 26 |
| L03-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 35 |
| L04-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 30 |
| L05-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 32 |
| L06-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 34 |
| L07-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 36 |
| L08-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 36 |
| L09-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 36 |
| L10-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 36 |
| L11-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 36 |
| L12-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 36 |
| L14-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 36 |
| L15-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 36 |
| L16-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 37 |
| L17-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 36 |
| LL2E-8340 | LL2 - Install walk-in cooler/freezer (BY OTHERS) | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 17 |
| MPP-1004 | Podium - Pool Area & Cornice | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 53 |
| L06-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 46 |
| L10-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 19 |

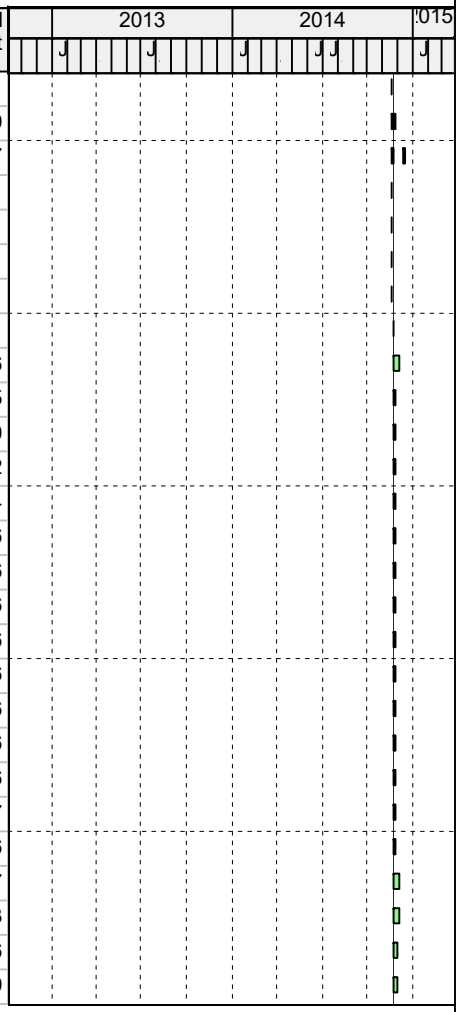



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8201 | Corridors - Install ACT Grid | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 42 |
| L15-8201 | Corridors - Install ACT Grid | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 42 |
| L16-8201 | Corridors - Install ACT Grid | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 43 |
| L03-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 46 |
| L04-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 46 |
| L05-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 46 |
| L06-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 46 |
| L16-8136 | Bathrooms - Install Counter Subtops | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 31 |
| LL1-Z2-8102a | GWB Hang (Ceilings) & Inspection | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 26 |
| L1K-8102a | GWB Hang (Ceilings at Public Restroom) & Inspectio | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 14 |
| L02-6016a | L2 - Electrical Room Buildout | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 45 |
| L02-8104a | L2 - Int Painting - South Half | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 31 |
| SW-2110 | Zone 1 - Adjust utilities structures | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 62 |
| SW-2210 | Zone 2 - Fine grade for sidewalk | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 60 |
| SW-2214 | Zone 2 - Adjust utilities structures | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 66 |
| SW-2318 | Zone 3 - Install catch basin | 1 | 1 | 24-Nov-14 | 24-Nov-14 | 68 |
| RF-4042 | Pool Roof - Install metal coping at high roof | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 55 |
| RF-4060 | Roof at Manlift - Install corrugated metal panels | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 68 |
| MPT-1030 | Tower - Install sign backing NE (Elev 44) | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 70 |
| CO-7160 | Generator - Cx generator/owner training | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 75 |
| CO-7130 | Fire Alarm - Point-To-Point Wiring | 18 | 18 | 24-Nov-14* | 19-Dec-14 | 23 |
| LL2-2086 | LL2 - Epoxy Flooring at Laundry Room | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 51 |
| L16-8216 | Vinyl Wall Coverings - Install Murals | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 37 |
| L12-8140 | Install window sills | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 44 |
| L11-8140 | Install window sills | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 44 |
| L10-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 35 |
| L09-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 35 |

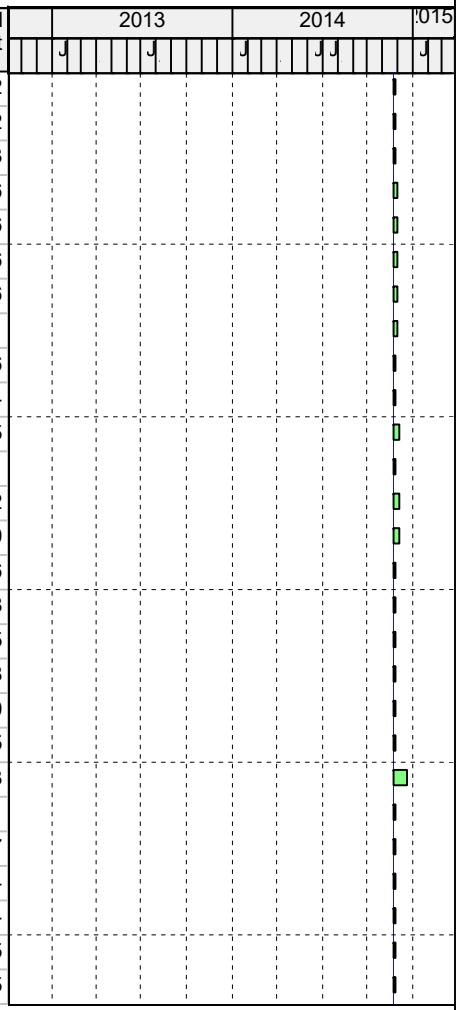



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 35 |
| L07-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 35 |
| L06-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 35 |
| L03-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 44 |
| L04-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 48 |
| SW-2012 | Porte Cochere - Install cornice | 8 | 8 | 24-Nov-14 | 05-Dec-14 | 39 |
| SW-2026 | Zone 4 - FRP NW planter | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 56 |
| I-1616 | Enclosure at manlift - Patch/repair concrete shear wal | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 30 |
| I-1622 | Manlift finishes - Install windows & caulk | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 20 |
| L03-8650 | L3 Pool - Build scaffold at pool pit | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 13 |
| EL-6032 | Elev 6 - Install pit ladder | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 27 |
| EL-6034 | Elev 6 - Install pit jack & hoistway pistons; connect hy | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 26 |
| CO-7126 | Fire pump test pre-planning complete (see checklist) | 0 | 0 |  | 24-Nov-14 | 59 |
| CO-7128 | Run fire pump test | 2 | 2 | 24-Nov-14 | 26-Nov-14 | 59 |
| L03-7030 | Paint | 1 | 1 | 25-Nov-14 | 25-Nov-14 | 30 |
| LL4-8102a | LL4 - GWB Tape/Finish | 3 | 3 | 25-Nov-14 | 01-Dec-14 | 47 |
| LL3-8102a | LL3 - GWB Tape/Finish | 3 | 3 | 25-Nov-14 | 01-Dec-14 | 47 |
| SW-2310 | Zone 3 - Install irrigation sleeves | 2 | 2 | 25-Nov-14 | 26-Nov-14 | 62 |
| SW-2016 | Porte Cochere - Complete framing | 3 | 3 | 25-Nov-14 | 01-Dec-14 | 43 |
| MPP-1006 | Podium - Install Level 3 Cornice (All 4 Sides) | 5 | 5 | 26-Nov-14 | 04-Dec-14 | 51 |
| L03-7032 | Install VCT Flooring (x42) | 1 | 1 | 26-Nov-14 | 26-Nov-14 | 43 |
| L04-7030 | Paint | 1 | 1 | 26-Nov-14 | 26-Nov-14 | 30 |
| SW-2308 | Zone 3 - Install site lighting | 5 | 5 | 26-Nov-14 | 04-Dec-14 | 62 |
| RF-4040 | L2.5 Horseshoe - Install sheet metal capping | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 55 |
| L09-8216 | Vinyl Wall Coverings - Install Murals | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 39 |
| L11-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 41 |
| L10-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 46 |

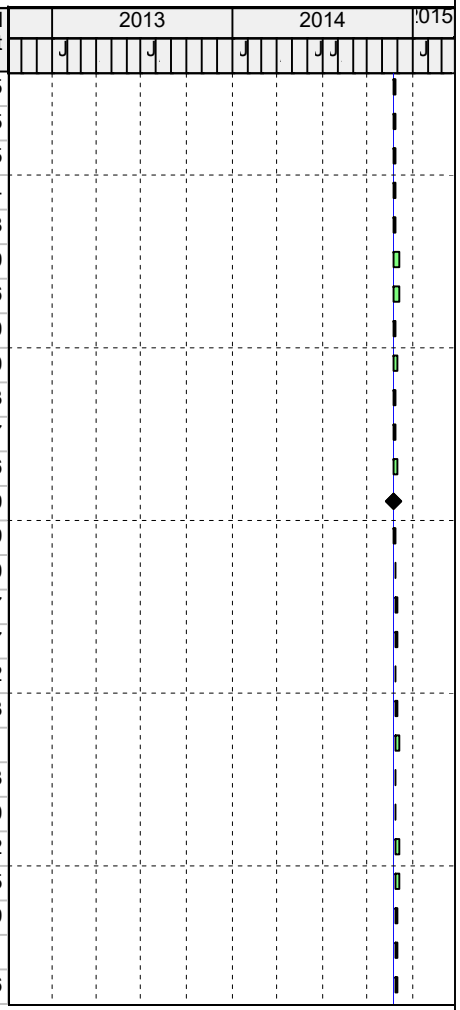



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 46 |
| L08-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 46 |
| L07-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 46 |
| L06-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 46 |
| L05-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 46 |
| L03-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 46 |
| L04-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 37 |
| I-1624 | Manlift finishes - Install batt insulation & inspect | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 20 |
| L03-8652 | L3 Pool - Frame ceiling | 4 | 4 | 26-Nov-14 | 03-Dec-14 | 13 |
| L03-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 35 |
| L04-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 30 |
| L05-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 32 |
| L06-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 34 |
| L07-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 36 |
| L08-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 36 |
| L09-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 36 |
| L10-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 36 |
| L11-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 36 |
| L12-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 36 |
| L14-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 36 |
| L15-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 36 |
| L16-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 37 |
| L17-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 36 |
| L07-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 01-Dec-14 | 04-Dec-14 | 43 |
| L17-8201 | Corridors - Install ACT Grid | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 37 |
| L03-7034 | Install Door and Hardware (x42) | 1 | 1 | 01-Dec-14 | 01-Dec-14 | 43 |
| L03-7132 | Paint Prime/1st Coat | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 40 |

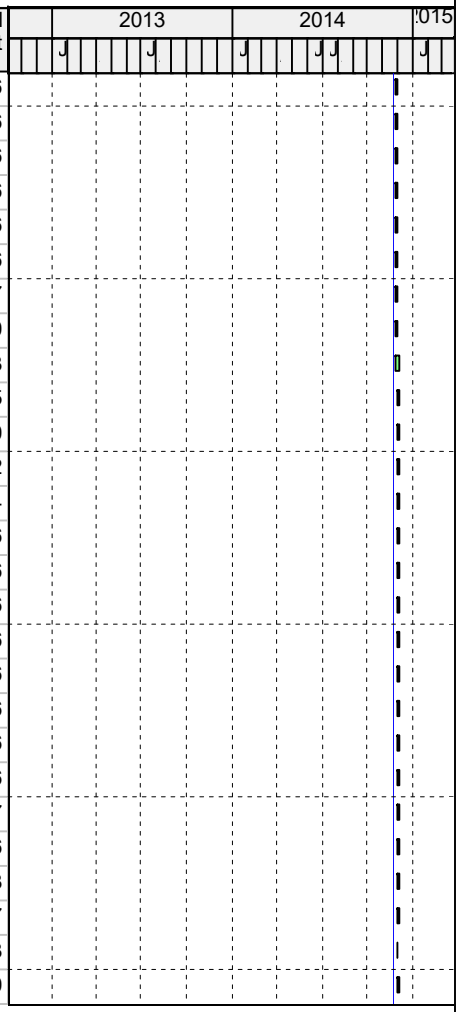



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7032 | Install VCT Flooring (x42) | 1 | 1 | 01-Dec-14 | 01-Dec-14 | 42 |
| L05-7030 | Paint | 1 | 1 | 01-Dec-14 | 01-Dec-14 | 30 |
| L04-7132 | Paint Prime/1st Coat | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 29 |
| L05-7132 | Paint Prime/1st Coat | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 31 |
| L06-7132 | Paint Prime/1st Coat | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 33 |
| L07-7132 | Paint Prime/1st Coat | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 35 |
| L08-7132 | Paint Prime/1st Coat | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 37 |
| L09-7132 | Paint Prime/1st Coat | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 39 |
| L10-7132 | Paint Prime/1st Coat | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 41 |
| L11-7132 | Paint Prime/1st Coat | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 40 |
| L12-7132 | Paint Prime/1st Coat | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 40 |
| L14-7132 | Paint Prime/1st Coat | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 40 |
| L15-7132 | Paint Prime/1st Coat | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 41 |
| L16-7132 | Paint Prime/1st Coat | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 42 |
| L17-7132 | Paint Prime/1st Coat | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 41 |
| L07-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 01-Dec-14 | 04-Dec-14 | 43 |
| LL2-2060 | LL2 - Paint Laundry Room | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 51 |
| RF-4062 | Roof at Manlift - Install sheet metal capping | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 68 |
| MPT-1044 | Enclosure at manlift - Install sign backing south | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 30 |
| CO-7208 | Cx - Start-Up Pumps | 2 | 2 | 01-Dec-14* | 02-Dec-14 | 19 |
| CO-7210 | Cx - Start-Up VFD's | 2 | 2 | 01-Dec-14* | 02-Dec-14 | 19 |
| L17-8106 | Paint - Accent Walls | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 24 |
| L17-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 24 |
| L15-8140 | Install window sills | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 42 |
| L14-8140 | Install window sills | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 42 |
| CO-7252 | Cx - Start-Up - FSD & SD Operation Verification | 10 | 10 | 01-Dec-14* | 12-Dec-14 | 18 |
| SW-2018 | Porte Cochere - GWB hang/tape | 3 | 3 | 01-Dec-14 | 03-Dec-14 | 43 |

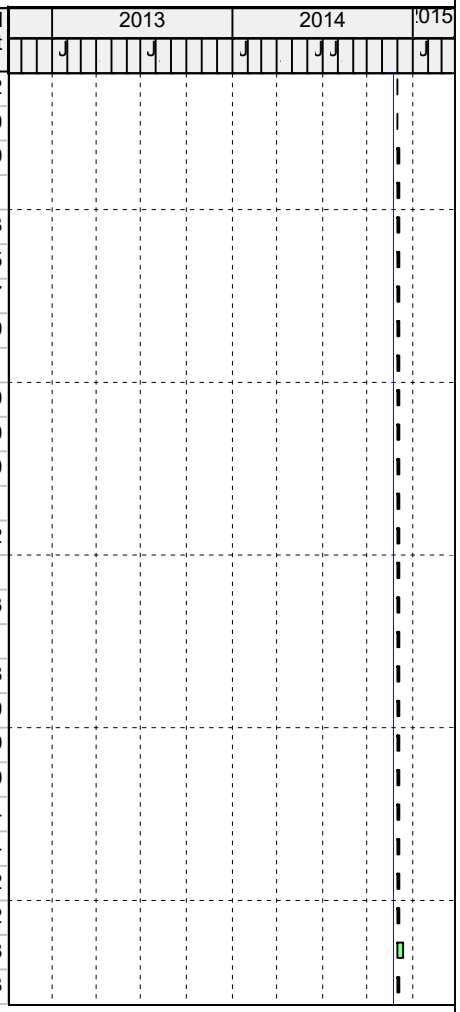



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1626 | Manlift finishes - Shim window openings | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 20 |
| EL-1236 | Elev 1&2 - Walsh/TKE pre-inspection | 6 | 6 | 01-Dec-14 | 08-Dec-14 | 47 |
| EL-6036 | Elev 6 - Install shunt trip breaker | 5 | 5 | 01-Dec-14 | 05-Dec-14 | 26 |
| L1BOH2-8104 | Prime Paint | 4 | 4 | 02-Dec-14 | 05-Dec-14 | 32 |
| L11-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 02-Dec-14 | 05-Dec-14 | 19 |
| L03-7042 | Install Tile Flooring (x41) | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 43 |
| L04-7034 | Install Door and Hardware (x42) | 1 | 1 | 02-Dec-14 | 02-Dec-14 | 42 |
| L05-7032 | Install VCT Flooring (x42) | 1 | 1 | 02-Dec-14 | 02-Dec-14 | 44 |
| L06-7030 | Paint | 1 | 1 | 02-Dec-14 | 02-Dec-14 | 30 |
| L10-8216 | Vinyl Wall Coverings - Install Murals | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 39 |
| L11-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 44 |
| L10-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 35 |
| L09-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 35 |
| L08-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 35 |
| L07-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 35 |
| L06-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 35 |
| L05-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 35 |
| L03-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 44 |
| I-1628 | Manlift finishes - Install vapor barrier & inspect | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 20 |
| L03-8654 | L3 Pool - HVAC drops at ceiling & inspect | 3 | 3 | 02-Dec-14 | 04-Dec-14 | 15 |
| LL1-Z3-FCC28 | FCC - Electrical trim/finish | 4 | 4 | 02-Dec-14 | 05-Dec-14 | 35 |
| L03-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 35 |
| L03-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 37 |
| L04-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 30 |
| L04-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 32 |
| L05-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 32 |
| L05-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 34 |

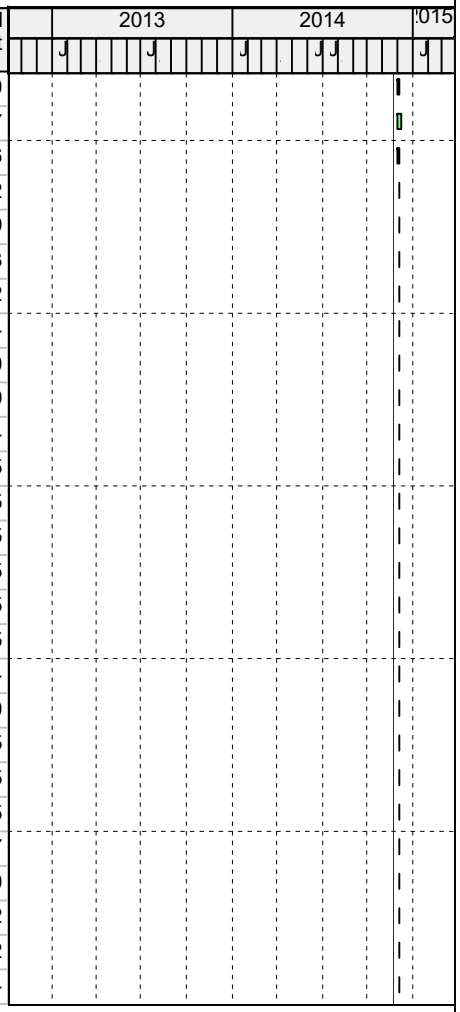



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 34 |
| L06-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 36 |
| L07-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 36 |
| L07-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 38 |
| L08-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 36 |
| L08-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 38 |
| L09-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 36 |
| L09-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 38 |
| L10-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 36 |
| L10-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 38 |
| L11-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 36 |
| L11-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 38 |
| L12-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 36 |
| L12-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 38 |
| L14-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 36 |
| L14-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 38 |
| L15-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 36 |
| L15-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 38 |
| L16-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 37 |
| L16-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 39 |
| L17-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 36 |
| L17-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 38 |
| LL2E-8342 | LL2 - Final connections at walk-in cooler/freezer | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 63 |
| LL1-6014lb | L1 bar redesign - rework ceiling framing & inspection | 5 | 5 | 03-Dec-14 | 09-Dec-14 | 18 |
| L04-7042 | Install Tile Flooring (x41) | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 42 |
| L05-7034 | Install Door and Hardware (x42) | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 44 |
| L06-7032 | Install VCT Flooring (x42) | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 40 |

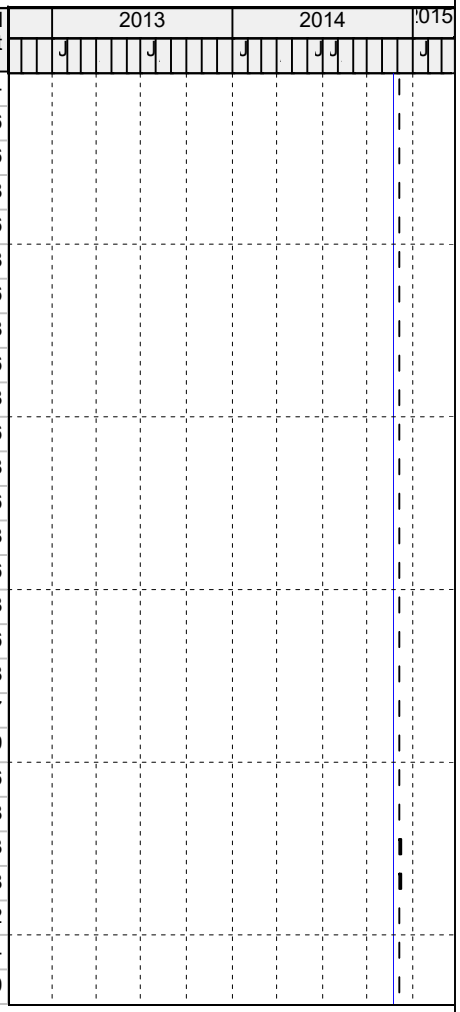



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7030 | Paint | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 30 |
| L17-8136 | Bathrooms - Install Counter Subtops | 4 | 4 | 03-Dec-14 | 08-Dec-14 | 26 |
| SW-2212 | Zone 2 - FRP sidewalk | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 60 |
| CO-7214 | Cx - Flush & Fill HVAC Hydronics Systems | 6 | 6 | 03-Dec-14 | 10-Dec-14 | 19 |
| RF-4072 | Pool Roof - Install metal coping | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 63 |
| L17-8111 | Paint - Door Jambs | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 35 |
| LL4-8116 | LL4 - Install ACT grid | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 47 |
| LL3-8116 | LL3 - Install ACT grid | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 47 |
| SW-2020 | Porte Cochere - Paint | 4 | 4 | 03-Dec-14 | 08-Dec-14 | 43 |
| SW-2028 | Zone 4 - Scan Porte Cochere deck | 2 | 2 | 03-Dec-14 | 04-Dec-14 | 56 |
| L03-8656 | L3 Pool - Electrical rough-in at ceiling & inspect | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 14 |
| I-1604 | Manlift finishes - GWB, hang walls | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 20 |
| LL2-2048 | LL2 - Set Laundry Room equipment (BY OTHERS) | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 51 |
| L03-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 43 |
| L03-7138 | Electrical Trim-Out | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 40 |
| L03-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 40 |
| L05-7042 | Install Tile Flooring (x41) | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 44 |
| L06-7034 | Install Door and Hardware (x42) | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 40 |
| L07-7032 | Install VCT Flooring (x42) | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 39 |
| L08-7030 | Paint | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 30 |
| L04-7138 | Electrical Trim-Out | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 29 |
| L04-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 29 |
| L05-7138 | Electrical Trim-Out | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 31 |
| L05-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 31 |
| L06-7138 | Electrical Trim-Out | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 33 |
| L06-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 33 |
| L07-7138 | Electrical Trim-Out | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 35 |

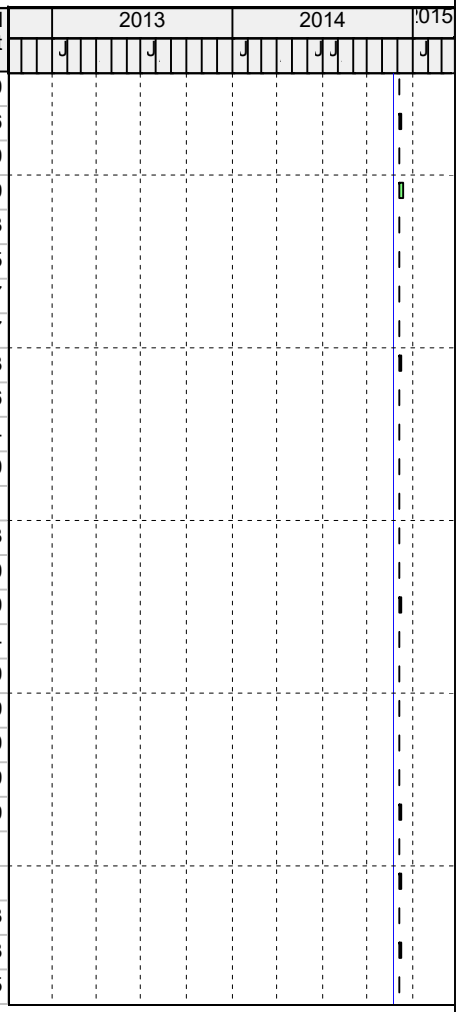



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 35 |
| L08-7138 | Electrical Trim-Out | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 37 |
| L08-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 37 |
| L09-7138 | Electrical Trim-Out | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 39 |
| L09-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 39 |
| L10-7138 | Electrical Trim-Out | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 41 |
| L10-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 41 |
| L11-7138 | Electrical Trim-Out | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 40 |
| L11-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 40 |
| L12-7138 | Electrical Trim-Out | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 40 |
| L12-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 40 |
| L14-7138 | Electrical Trim-Out | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 40 |
| L14-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 40 |
| L15-7138 | Electrical Trim-Out | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 41 |
| L15-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 41 |
| L16-7138 | Electrical Trim-Out | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 42 |
| L16-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 42 |
| L17-7138 | Electrical Trim-Out | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 41 |
| L17-7140 | Fire Alarm / Elec Specialties Trim-Out | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 41 |
| L03-7144 | Fire Sprinkler Trim | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 42 |
| L04-7144 | Fire Sprinkler Trim | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 31 |
| L05-7144 | Fire Sprinkler Trim | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 33 |
| L06-7144 | Fire Sprinkler Trim | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 35 |
| L07-7144 | Fire Sprinkler Trim | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 37 |
| L08-7144 | Fire Sprinkler Trim | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 39 |
| L09-7144 | Fire Sprinkler Trim | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 41 |
| L10-7144 | Fire Sprinkler Trim | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 43 |

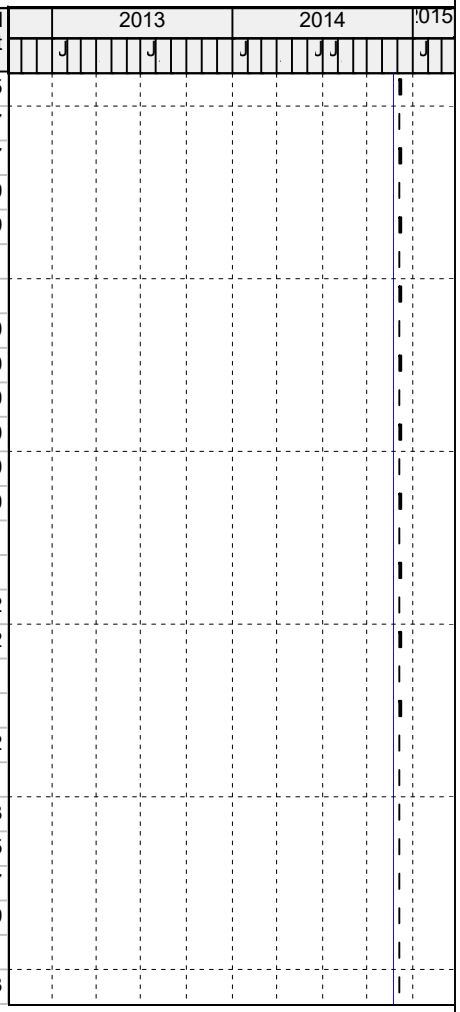



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7144 | Fire Sprinkler Trim | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 42 |
| L12-7144 | Fire Sprinkler Trim | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 42 |
| L14-7144 | Fire Sprinkler Trim | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 42 |
| L15-7144 | Fire Sprinkler Trim | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 43 |
| L16-7144 | Fire Sprinkler Trim | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 44 |
| L17-7144 | Fire Sprinkler Trim | 1 | 1 | 04-Dec-14 | 04-Dec-14 | 44 |
| MPT-1042 | Enclosure at manlift - air barrier & inspect | 5 | 5 | 04-Dec-14 | 10-Dec-14 | 30 |
| L12-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 38 |
| L11-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 41 |
| L03-8658 | L3 Pool - Fire sprinkler drops at ceiling & inspect | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 13 |
| L1BOH2-8114 | T Bar Grid Ceiling | 3 | 3 | 05-Dec-14 | 09-Dec-14 | 25 |
| L04-8418 | Flooring at Elevator Lobby | 3 | 3 | 05-Dec-14 | 09-Dec-14 | 36 |
| L04-7044 | Install Vending Cabinets (x41) | 1 | 1 | 05-Dec-14 | 05-Dec-14 | 42 |
| L06-7042 | Install Tile Flooring (x41) | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 40 |
| L07-7034 | Install Door and Hardware (x42) | 1 | 1 | 05-Dec-14 | 05-Dec-14 | 39 |
| L08-7032 | Install VCT Flooring (x42) | 1 | 1 | 05-Dec-14 | 05-Dec-14 | 38 |
| L09-7030 | Paint | 1 | 1 | 05-Dec-14 | 05-Dec-14 | 30 |
| MPT-1018a | Tower - Install Roof Cornice Metal | 5 | 5 | 05-Dec-14 | 11-Dec-14 | 61 |
| SW-2312 | Zone 3 - Fine grade for sidewalk | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 62 |
| PC-4012 | Porte Cochere - Install sheet metal capping | 3 | 3 | 05-Dec-14 | 09-Dec-14 | 63 |
| MPP-1012 | Podium - Caulking, south | 5 | 5 | 05-Dec-14 | 11-Dec-14 | 51 |
| CO-7222 | Cx - Start-Up - Kitchen Exhaust Fans | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 35 |
| LL1-8120 | Install MEP Drops To T Bar Grid Ceiling | 3 | 3 | 05-Dec-14 | 09-Dec-14 | 25 |
| LL1-Z2-8115 | Install MEP Drops To T Bar Grid Ceiling | 3 | 3 | 05-Dec-14 | 09-Dec-14 | 26 |
| LL1-Z3-8115 | Install MEP Drops To T Bar Grid Ceiling | 3 | 3 | 05-Dec-14 | 09-Dec-14 | 25 |
| L16-8140 | Install window sills | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 39 |
| CO-7262 | Cx - Start-Up - Electric Unit Heaters | 3 | 3 | 05-Dec-14 | 09-Dec-14 | 54 |

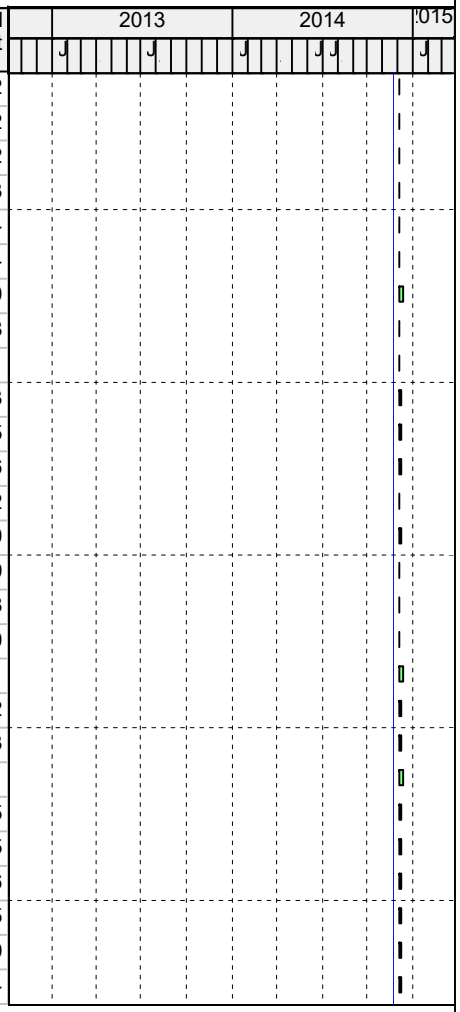



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 06-Dec-14 | 10-Dec-14 | 49 |
| L10-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 06-Dec-14 | 10-Dec-14 | 49 |
| L03-8418 | Flooring at Elevator Lobby | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 35 |
| L05-8418 | Flooring at Elevator Lobby | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 36 |
| L06-8418 | Flooring at Elevator Lobby | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 36 |
| L07-8418 | Flooring at Elevator Lobby | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 36 |
| L08-8418 | Flooring at Elevator Lobby | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 36 |
| L09-8418 | Flooring at Elevator Lobby | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 36 |
| L10-8418 | Flooring at Elevator Lobby | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 36 |
| L11-8418 | Flooring at Elevator Lobby | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 36 |
| L12-8418 | Flooring at Elevator Lobby | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 36 |
| L14-8418 | Flooring at Elevator Lobby | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 36 |
| L15-8418 | Flooring at Elevator Lobby | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 36 |
| L16-8418 | Flooring at Elevator Lobby | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 37 |
| L17-8418 | Flooring at Elevator Lobby | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 36 |
| LL2-2050 | LL2 - Laundry Room equipment final connections (MI | 1 | 1 | 08-Dec-14 | 08-Dec-14 | 51 |
| L1K-8340 | Install walk-in cooler/freezer (BY OTHERS) | 2 | 2 | 08-Dec-14 | 09-Dec-14 | 14 |
| L08-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 08-Dec-14 | 11-Dec-14 | 38 |
| L11-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 08-Dec-14 | 11-Dec-14 | 38 |
| L12-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 08-Dec-14 | 11-Dec-14 | 38 |
| L12-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 08-Dec-14 | 11-Dec-14 | 19 |
| L05-7044 | Install Vending Cabinets (x41) | 1 | 1 | 08-Dec-14 | 08-Dec-14 | 46 |
| L07-7042 | Install Tile Flooring (x41) | 2 | 2 | 08-Dec-14 | 09-Dec-14 | 39 |
| L08-7034 | Install Door and Hardware (x42) | 1 | 1 | 08-Dec-14 | 08-Dec-14 | 38 |
| L09-7032 | Install VCT Flooring (x42) | 1 | 1 | 08-Dec-14 | 08-Dec-14 | 37 |
| L10-7030 | Paint | 1 | 1 | 08-Dec-14 | 08-Dec-14 | 30 |
| L11-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 08-Dec-14 | 11-Dec-14 | 38 |

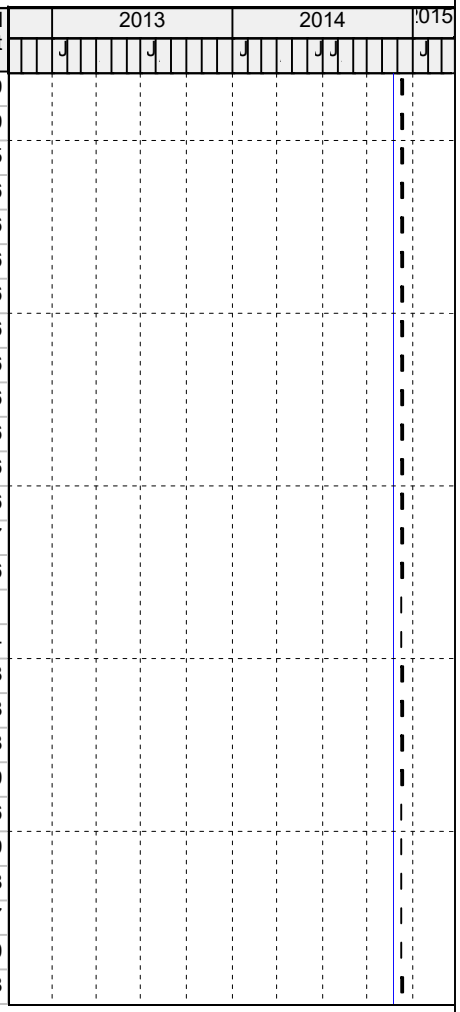



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 08-Dec-14 | 11-Dec-14 | 38 |
| L09-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 08-Dec-14 | 11-Dec-14 | 38 |
| L10-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 08-Dec-14 | 11-Dec-14 | 38 |
| L12-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 08-Dec-14 | 11-Dec-14 | 38 |
| LL2-2062 | LL2 - Install ceiling grid | 2 | 2 | 08-Dec-14 | 09-Dec-14 | 51 |
| L02-8130 | L2 - Install ACT Grid | 5 | 5 | 08-Dec-14 | 12-Dec-14 | 25 |
| SW-2120 | Zone 1 - Install irrigation | 5 | 5 | 08-Dec-14 | 12-Dec-14 | 60 |
| SW-2122 | Zone 1 - Install landscaping | 5 | 5 | 08-Dec-14 | 12-Dec-14 | 60 |
| SW-2314 | Zone 3 - FRP sidewalk | 3 | 3 | 08-Dec-14 | 10-Dec-14 | 62 |
| L12-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 08-Dec-14 | 09-Dec-14 | 40 |
| SW-2022 | Remove pedestrian protection on 10th Ave | 1 | 1 | 08-Dec-14 | 08-Dec-14 | 39 |
| I-1630 | Manlift finishes - Framing, corridor ceilings & inspect | 4 | 4 | 08-Dec-14 | 11-Dec-14 | 20 |
| LL1-Z3-FCC30 | FCC - Data/phone trim/finish | 2 | 2 | 08-Dec-14 | 09-Dec-14 | 35 |
| L1K-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 09-Dec-14 | 10-Dec-14 | 14 |
| L06-7044 | Install Vending Cabinets (x41) | 1 | 1 | 09-Dec-14 | 09-Dec-14 | 40 |
| L08-7042 | Install Tile Flooring (x41) | 2 | 2 | 09-Dec-14 | 10-Dec-14 | 38 |
| L09-7034 | Install Door and Hardware (x42) | 1 | 1 | 09-Dec-14 | 09-Dec-14 | 37 |
| L10-7032 | Install VCT Flooring (x42) | 1 | 1 | 09-Dec-14 | 09-Dec-14 | 36 |
| L11-7030 | Paint | 1 | 1 | 09-Dec-14 | 09-Dec-14 | 30 |
| MPP-1016 | Podium - Caulking, east | 6 | 6 | 09-Dec-14 | 16-Dec-14 | 53 |
| CO-7234 | Cx - TAB - CW Water Balancing | 10 | 10 | 09-Dec-14 | 22-Dec-14 | 47 |
| L17-8216 | Vinyl Wall Coverings - Install Murals | 2 | 2 | 09-Dec-14 | 10-Dec-14 | 28 |
| L1BOH2C-6024 | MEP Trim at Ceiling | 3 | 3 | 09-Dec-14 | 11-Dec-14 | 25 |
| CO-7256 | Cx - Start-Up - Elevator Machine Room Ductless Split | 1 | 1 | 09-Dec-14 | 09-Dec-14 | 35 |
| SW-2030 | Zone 4 - Remove existing trees | 1 | 1 | 09-Dec-14 | 09-Dec-14 | 39 |
| SW-2046 | Zone 4 - Install site lighting | 3 | 3 | 09-Dec-14 | 11-Dec-14 | 43 |
| L03-8660 | L3 Pool - GWB hang ceilings | 3 | 3 | 09-Dec-14 | 11-Dec-14 | 13 |

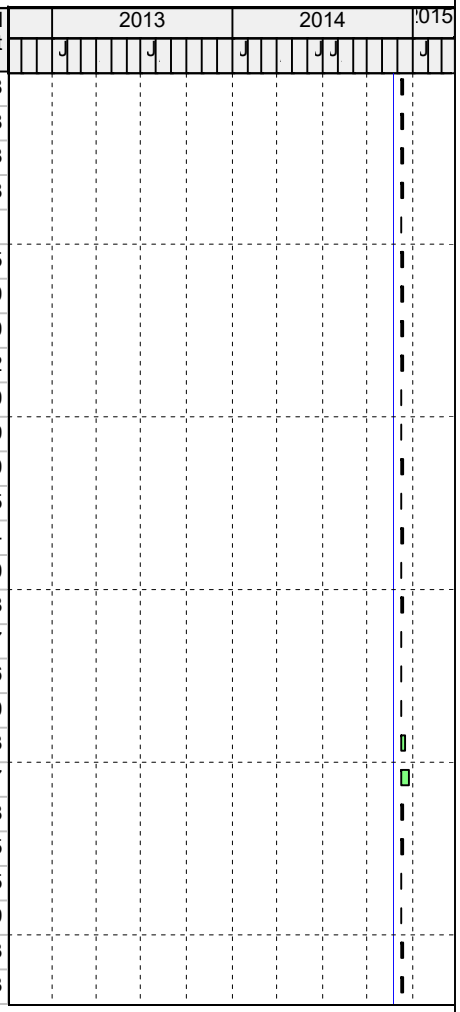



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1BOH2-8140 | Acoustical Ceiling Tile | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 25 |
| L04-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 36 |
| L05-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 36 |
| L06-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 36 |
| L07-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 36 |
| L08-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 36 |
| L09-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 36 |
| L10-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 36 |
| L11-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 36 |
| L12-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 36 |
| L15-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 36 |
| L16-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 37 |
| L17-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 36 |
| L07-7044 | Install Vending Cabinets (x41) | 1 | 1 | 10-Dec-14 | 10-Dec-14 | 39 |
| L09-7042 | Install Tile Flooring (x41) | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 37 |
| L10-7034 | Install Door and Hardware (x42) | 1 | 1 | 10-Dec-14 | 10-Dec-14 | 36 |
| L11-7032 | Install VCT Flooring (x42) | 1 | 1 | 10-Dec-14 | 10-Dec-14 | 35 |
| L12-7030 | Paint | 1 | 1 | 10-Dec-14 | 10-Dec-14 | 30 |
| LL1-6014lb2 | L1 bar redesign - GWB hang at ceilings | 4 | 4 | 10-Dec-14 | 15-Dec-14 | 18 |
| CO-7226 | Cx - Start-Up - Misc. Equipment | 5 | 5 | 10-Dec-14 | 16-Dec-14 | 54 |
| LL2-2088 | LL2 - Install MEP Drops to Grid | 3 | 3 | 10-Dec-14 | 12-Dec-14 | 51 |
| L15-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 34 |
| L14-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 34 |
| L12-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 38 |
| SW-2032 | Zone 4 - Demo existing hardscapes | 3 | 3 | 10-Dec-14 | 12-Dec-14 | 39 |
| I-1632 | Manlift finishes - Electrical rough-in & inspect | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 20 |
| LL1-Z3-FCC32 | FCC - Install flooring & base | 3 | 3 | 10-Dec-14 | 12-Dec-14 | 35 |

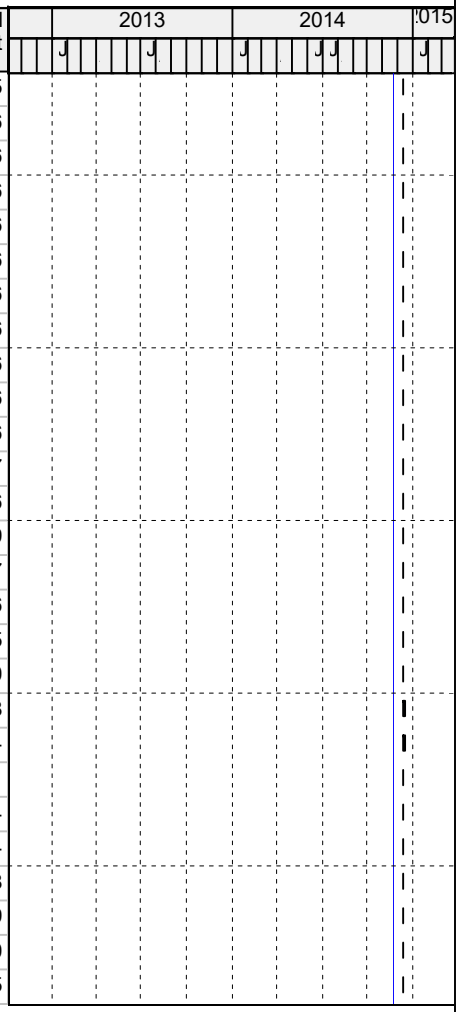



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1602 | Enclosure at manlift - Install shear wall clips and inspe | 4 | 4 | 11-Dec-14 | 16-Dec-14 | 30 |
| L03-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 11-Dec-14 | 12-Dec-14 | 35 |
| L14-8408 | Install Wood Base at Elevator Lobby | 2 | 2 | 11-Dec-14 | 12-Dec-14 | 36 |
| CO-7100T | Cx - Start-Up - Life Safety Exhaust Fans and VFD's | 12 | 12 | 11-Dec-14 | 30-Dec-14 | 22 |
| L14-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 11-Dec-14 | 16-Dec-14 | 35 |
| L15-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 11-Dec-14 | 16-Dec-14 | 35 |
| L08-7044 | Install Vending Cabinets (x41) | 1 | 1 | 11-Dec-14 | 11-Dec-14 | 38 |
| L10-7042 | Install Tile Flooring (x41) | 2 | 2 | 11-Dec-14 | 12-Dec-14 | 36 |
| L11-7034 | Install Door and Hardware (x42) | 1 | 1 | 11-Dec-14 | 11-Dec-14 | 35 |
| L12-7032 | Install VCT Flooring (x42) | 1 | 1 | 11-Dec-14 | 11-Dec-14 | 34 |
| L14-7030 | Paint | 1 | 1 | 11-Dec-14 | 11-Dec-14 | 30 |
| L14-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 11-Dec-14 | 16-Dec-14 | 35 |
| L15-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 11-Dec-14 | 16-Dec-14 | 35 |
| L1B-8102a | GWB Hang (Ceilings) | 5 | 5 | 11-Dec-14 | 17-Dec-14 | 15 |
| SW-2216 | Zone 2 - Install irrigation | 5 | 5 | 11-Dec-14 | 17-Dec-14 | 60 |
| SW-2218 | Zone 2 - Install landscaping | 5 | 5 | 11-Dec-14 | 17-Dec-14 | 60 |
| RF-4066 | Pool Green Roof - Install decorative metal railing | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 53 |
| CO-7212 | Cx - Start-Up Boilers | 2 | 2 | 11-Dec-14 | 12-Dec-14 | 24 |
| CO-7216 | Cx - Start-Up Fluid Cooler | 3 | 3 | 11-Dec-14 | 15-Dec-14 | 19 |
| L03-8662 | L3 Pool - GWB tape ceilings | 3 | 3 | 11-Dec-14 | 13-Dec-14 | 17 |
| L1BOH2-8200 | First Coat Finish Paint | 5 | 5 | 12-Dec-14 | 18-Dec-14 | 25 |
| L04-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 36 |
| L05-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 36 |
| L06-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 36 |
| L07-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 36 |
| L08-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 36 |
| L09-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 36 |

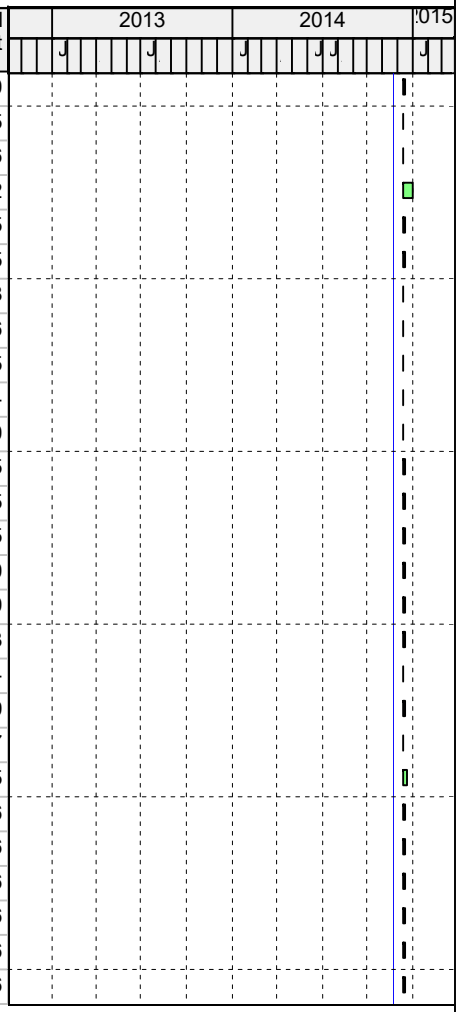


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 36 |
| L11-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 36 |
| L12-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 36 |
| L14-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 36 |
| L15-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 36 |
| L16-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 37 |
| L17-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 36 |
| L14-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 12-Dec-14 | 17-Dec-14 | 19 |
| L09-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 12-Dec-14 | 12-Dec-14 | 37 |
| L11-7042 | Install Tile Flooring (x41) | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 35 |
| L12-7034 | Install Door and Hardware (x42) | 1 | 1 | 12-Dec-14 | 12-Dec-14 | 34 |
| L14-7032 | Install VCT Flooring (x42) | 1 | 1 | 12-Dec-14 | 12-Dec-14 | 33 |
| L15-7030 | Paint | 1 | 1 | 12-Dec-14 | 12-Dec-14 | 30 |
| MPP-1014 | Podium - Caulking, west | 5 | 5 | 12-Dec-14 | 18-Dec-14 | 51 |
| L17-8140 | Install window sills | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 33 |
| L15-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 36 |
| L14-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 36 |
| I-1634 | Manlift finihse - GWB, hang ceilings | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 20 |
| L03-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 15-Dec-14 | 16-Dec-14 | 35 |
| CO-7102T | Cx - DDC Point-To-Point - Central Plant | 5 | 5 | 15-Dec-14 | 19-Dec-14 | 48 |
| L10-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 15-Dec-14 | 15-Dec-14 | 36 |
| L12-7042 | Install Tile Flooring (x41) | 2 | 2 | 15-Dec-14 | 16-Dec-14 | 34 |
| L14-7034 | Install Door and Hardware (x42) | 1 | 1 | 15-Dec-14 | 15-Dec-14 | 33 |
| L15-7032 | Install VCT Flooring (x42) | 1 | 1 | 15-Dec-14 | 15-Dec-14 | 32 |
| L16-7030 | Paint | 1 | 1 | 15-Dec-14 | 15-Dec-14 | 30 |
| L1L-8102a | GWB Hang/Tape (Ceilings) | 5 | 5 | 15-Dec-14 | 19-Dec-14 | 0 |
| SW-2322 | Zone 3 - Install irrigation | 5 | 5 | 15-Dec-14 | 19-Dec-14 | 60 |

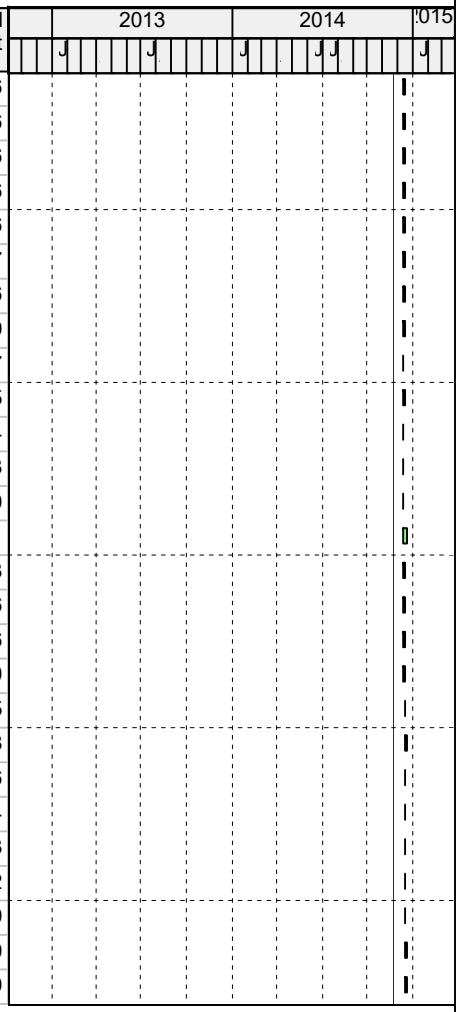



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2324 | Zone 3 - Install landscaping | 5 | 5 | 15-Dec-14 | 19-Dec-14 | 60 |
| MPT-1028 | Tower - Caulking, south | 13 | 13 | 15-Dec-14 | 05-Jan-15 | 47 |
| CO-7232 | Cx - TAB - CW Pump Totalization | 1 | 1 | 15-Dec-14 | 15-Dec-14 | 52 |
| LL2-2090 | LL2 - Install ceiling tile | 1 | 1 | 15-Dec-14 | 15-Dec-14 | 51 |
| LL2-2092 | LL2 - MEP trim | 3 | 3 | 15-Dec-14 | 17-Dec-14 | 51 |
| LL1-Z3-8142 | Install Restroom Ceramic Tile | 5 | 5 | 15-Dec-14 | 19-Dec-14 | 32 |
| CO-7240 | Cx - Heat Pump Start-Up - Levels 3 & 4 | 6 | 6 | 15-Dec-14 | 22-Dec-14 | 24 |
| CO-7254 | Cx - Start-Up - MUA AAON (8) | 8 | 8 | 15-Dec-14 | 24-Dec-14 | 18 |
| SW-2034 | Zone 4 - Install irrigation sleeves | 3 | 3 | 15-Dec-14 | 17-Dec-14 | 39 |
| SW-2036 | Zone 4 - Grade for curb and gutter | 1 | 1 | 15-Dec-14 | 15-Dec-14 | 39 |
| I-1636 | Manlift finishes - GWB, tape & finish | 4 | 4 | 15-Dec-14 | 18-Dec-14 | 20 |
| L03-8664 | L3 Pool - Prime & paint ceilings | 3 | 3 | 15-Dec-14 | 17-Dec-14 | 13 |
| EL-6038 | Elev 6 - Rough-in call boxes & lanterns | 5 | 5 | 15-Dec-14 | 19-Dec-14 | 26 |
| EL-6052 | Elev 6 - Complete hoistway ventilation | 5 | 5 | 15-Dec-14 | 19-Dec-14 | 29 |
| LL1-Z3-FCC34 | FCC - Final paint/touch up | 2 | 2 | 15-Dec-14 | 16-Dec-14 | 35 |
| LL1-Z3-FCC36 | FCC - Install door & hardware | 2 | 2 | 15-Dec-14 | 16-Dec-14 | 35 |
| L11-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 16-Dec-14 | 16-Dec-14 | 35 |
| L14-7042 | Install Tile Flooring (x41) | 2 | 2 | 16-Dec-14 | 17-Dec-14 | 33 |
| L15-7034 | Install Door and Hardware (x42) | 1 | 1 | 16-Dec-14 | 16-Dec-14 | 32 |
| L16-7032 | Install VCT Flooring (x42) | 1 | 1 | 16-Dec-14 | 16-Dec-14 | 32 |
| L17-7030 | Paint | 1 | 1 | 16-Dec-14 | 16-Dec-14 | 30 |
| LL1-Z2-8124a | Install Base | 3 | 3 | 16-Dec-14 | 18-Dec-14 | 26 |
| RF-4068 | Pool Green Roof - Install American Hydrotech assem | 3 | 3 | 16-Dec-14 | 18-Dec-14 | 53 |
| LL1-6014Id | L1 bar redesign - Complete finishes at ceilings | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 18 |
| L15-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 16-Dec-14 | 17-Dec-14 | 34 |
| L14-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 16-Dec-14 | 17-Dec-14 | 34 |
| SW-2038 | Zone 4 - FRP curb & gutter | 1 | 1 | 16-Dec-14 | 16-Dec-14 | 39 |

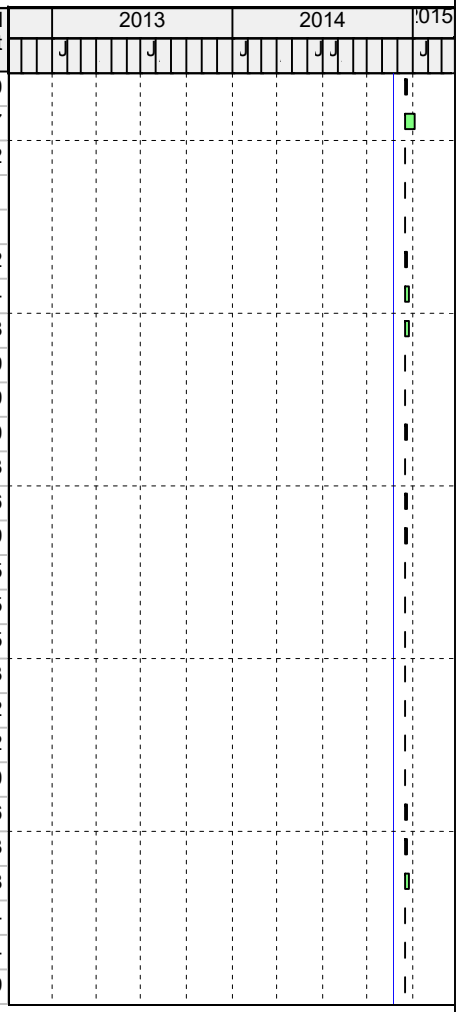



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 17-Dec-14 | 22-Dec-14 | 32 |
| L12-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 17-Dec-14 | 17-Dec-14 | 34 |
| L15-7042 | Install Tile Flooring (x41) | 2 | 2 | 17-Dec-14 | 18-Dec-14 | 32 |
| L16-7034 | Install Door and Hardware (x42) | 1 | 1 | 17-Dec-14 | 17-Dec-14 | 32 |
| L17-7032 | Install VCT Flooring (x42) | 1 | 1 | 17-Dec-14 | 17-Dec-14 | 30 |
| L16-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 17-Dec-14 | 22-Dec-14 | 32 |
| CO-7400 | Cx - 3rd Party Cx of Mechanical, Plumbing, Electrical | 45 | 45 | 17-Dec-14 | 20-Feb-15 | 18 |
| L16-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 17-Dec-14 | 18-Dec-14 | 30 |
| SW-2040 | Zone 4 - Grade for sidewalk | 3 | 3 | 17-Dec-14 | 19-Dec-14 | 39 |
| I-1614 | Enclosure at manlift - Install rigid insulation at shear w | 3 | 3 | 17-Dec-14 | 19-Dec-14 | 30 |
| LL1-Z3-FCC38 | FCC - Final clean and punch list | 3 | 3 | 17-Dec-14 | 19-Dec-14 | 35 |
| LL1-Z3-8340 | Install walk-in cooler/freezer (BY OTHERS) | 5 | 5 | 18-Dec-14* | 24-Dec-14 | 34 |
| L03-8622 | L3 Pool - HVAC trim / Finish | 2 | 2 | 18-Dec-14 | 19-Dec-14 | 13 |
| L03-8624 | L3 Pool - Fire Sprinkler Trim / Finish | 2 | 2 | 18-Dec-14 | 19-Dec-14 | 13 |
| L15-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 18-Dec-14 | 23-Dec-14 | 19 |
| L14-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 18-Dec-14 | 18-Dec-14 | 33 |
| L16-7042 | Install Tile Flooring (x41) | 2 | 2 | 18-Dec-14 | 19-Dec-14 | 32 |
| L17-7034 | Install Door and Hardware (x42) | 1 | 1 | 18-Dec-14 | 18-Dec-14 | 30 |
| LL2-2094 | LL2 - Install doors & hardware | 1 | 1 | 18-Dec-14 | 18-Dec-14 | 51 |
| L1K-8210 | Install Restroom Ceramic Tile | 5 | 5 | 18-Dec-14 | 24-Dec-14 | 28 |
| L1BOH2-8124 | Flooring | 5 | 5 | 19-Dec-14 | 29-Dec-14 | 25 |
| I-1606 | Manlift finishes - Prime & paint | 3 | 3 | 19-Dec-14 | 23-Dec-14 | 20 |
| L15-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 19-Dec-14 | 19-Dec-14 | 32 |
| L17-7042 | Install Tile Flooring (x41) | 2 | 2 | 19-Dec-14 | 22-Dec-14 | 30 |
| RF-4070 | TR - Terrace Roof - Install American Hydrotech assem | 3 | 3 | 19-Dec-14 | 23-Dec-14 | 53 |
| MPP-1018 | Podium - Caulking, north | 5 | 5 | 19-Dec-14 | 29-Dec-14 | 51 |
| L16-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 19-Dec-14 | 22-Dec-14 | 32 |

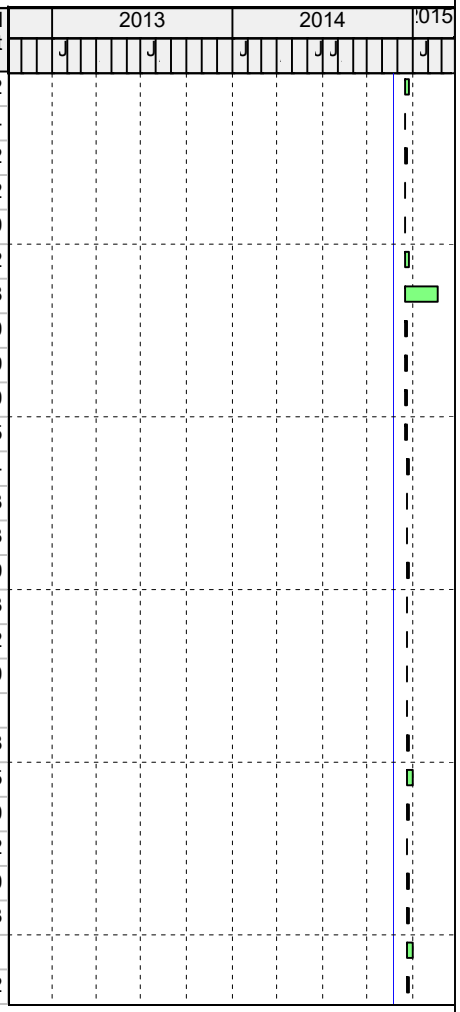



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8666 | L3 Pool - Elec Trim / Finish at ceiling | 2 | 2 | 19-Dec-14 | 22-Dec-14 | 13 |
| CO-7110T | Fire Sprinkler Pre-Testing (Tower) | 15 | 15 | 22-Dec-14 | 14-Jan-15 | 23 |
| CO-7116T | Fire Alarm Pre-Testing (Tower) | 15 | 15 | 22-Dec-14 | 14-Jan-15 | 23 |
| CO-7104T | Smoke Control Pre-Testing (Tower) | 15 | 15 | 22-Dec-14 | 14-Jan-15 | 23 |
| L16-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 22-Dec-14 | 22-Dec-14 | 32 |
| L02-8138 | L2 - Install ceiling tile | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 25 |
| L17-8130 | Install Door Hardware | 3 | 3 | 22-Dec-14 | 24-Dec-14 | 29 |
| L17-8218 | Corridors - Fire Sprinkler Trim | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 24 |
| LL1-Z3-8144 | Install Restroom Fixtures | 5 | 5 | 22-Dec-14 | 30-Dec-14 | 32 |
| SW-2042 | Zone 4 - Install trench drain | 3 | 3 | 22-Dec-14 | 24-Dec-14 | 39 |
| I-1618 | Enclosure at manlift - Install framing at shear wall | 6 | 6 | 22-Dec-14 | 31-Dec-14 | 30 |
| L03-8670 | L3 Pool - Rough-in pool trench drain | 4 | 4 | 22-Dec-14 | 29-Dec-14 | 13 |
| EL-6040 | Elev 6 - Install machine room controller equipment/hy | 3 | 3 | 22-Dec-14 | 24-Dec-14 | 26 |
| EL-6042 | Elev 6 - Install EMR heat pump | 6 | 6 | 22-Dec-14 | 31-Dec-14 | 26 |
| EL-6054 | Elev 6 - Install EMR doors, hardware & labeling | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 29 |
| LL1-Z3-FCC40 | FCC - Install Knox Box | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 35 |
| L04-7134 | Install VCT Flooring | 2 | 2 | 22-Dec-14 | 24-Dec-14 | 20 |
| CM-1016a | CM - Owner FF+E "Build-Out" - Floors 3, 11-17 | 17 | 17 | 22-Dec-14 | 08-Jan-15 | 29 |
| L17-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 23-Dec-14 | 23-Dec-14 | 30 |
| L1K-8124a | Install Flooring (Epoxy) | 7 | 7 | 23-Dec-14 | 31-Dec-14 | 18 |
| L1BOH2-8124a | Install Base | 3 | 3 | 23-Dec-14 | 29-Dec-14 | 26 |
| L16-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 30 |
| CO-7242 | Cx - Heat Pump Start-Up - Levels 5 & 6 | 5 | 5 | 23-Dec-14 | 31-Dec-14 | 24 |
| I-1638 | Manlift finishes - Install ceiling grid | 3 | 3 | 23-Dec-14 | 29-Dec-14 | 20 |
| I-1640 | Manlift finishes - Install window sills | 3 | 3 | 23-Dec-14 | 29-Dec-14 | 51 |
| L03-8668 | L3 Pool - Remove scaffolding at pool pit | 1 | 1 | 23-Dec-14 | 23-Dec-14 | 13 |
| L16-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 24-Dec-14 | 31-Dec-14 | 19 |

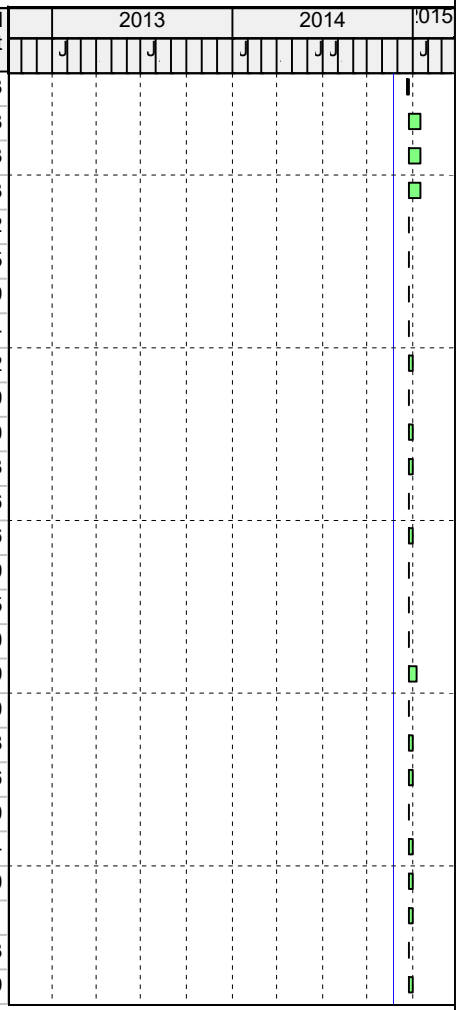



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 24-Dec-14 | 31-Dec-14 | 26 |
| L17-8138 | Bathrooms - Install Toilet Accessories | 4 | 4 | 24-Dec-14 | 31-Dec-14 | 26 |
| LL1-Z3-FCC22 | FCC - Final inspections by CoB and Fire Marshall | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 35 |
| L17-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 24 |
| L03-8672 | L3 Pool - Prep pool area for topping slab | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 13 |
| L04-7136 | Install Door and Hardware | 1 | 1 | 24-Dec-14 | 29-Dec-14 | 32 |
| L05-7134 | Install VCT Flooring | 2 | 2 | 24-Dec-14 | 30-Dec-14 | 20 |
| LL1-Z3-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 29-Dec-14* | 30-Dec-14 | 34 |
| LL1-8124a | Install Base | 5 | 5 | 29-Dec-14 | 05-Jan-15 | 18 |
| L1K-8206 | Install Restroom Fixtures | 5 | 5 | 29-Dec-14 | 05-Jan-15 | 28 |
| CO-7258 | Cx - Start-Up - KMUA Trane (2) | 1 | 1 | 29-Dec-14 | 29-Dec-14 | 18 |
| SW-2044 | Zone 4 - FRP sidewalk | 3 | 3 | 29-Dec-14 | 31-Dec-14 | 39 |
| EL-6044 | Elev 6 - Electrical trim | 3 | 3 | 29-Dec-14 | 31-Dec-14 | 26 |
| EL-6046 | Elev 6 - Fire alarm trim | 3 | 3 | 29-Dec-14 | 31-Dec-14 | 26 |
| EL-6048 | Elev 6 - Fire sprinkler trim | 3 | 3 | 29-Dec-14 | 31-Dec-14 | 26 |
| EL-6050 | Elev 6 - Install pit grates | 3 | 3 | 29-Dec-14 | 31-Dec-14 | 26 |
| L04-7146 | Final Coat Finish Paint | 2 | 2 | 29-Dec-14 | 31-Dec-14 | 32 |
| L1BOH2-8116 | Finish Carpentry / Millwork | 5 | 5 | 30-Dec-14 | 06-Jan-15 | 25 |
| L1BOH2-8126 | Doors & Hardware | 5 | 5 | 30-Dec-14 | 06-Jan-15 | 25 |
| CO-7220 | Cx - Start-Up - Common Space Heat Pump | 4 | 4 | 30-Dec-14 | 05-Jan-15 | 18 |
| L17-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 30-Dec-14 | 31-Dec-14 | 26 |
| L03-8648 | L3 Pool- Install pool topping slab | 1 | 1 | 30-Dec-14 | 30-Dec-14 | 13 |
| CO-7260 | Cx - Start-Up - Ballroom AAON RTU | 1 | 1 | 30-Dec-14 | 30-Dec-14 | 35 |
| L05-7136 | Install Door and Hardware | 1 | 1 | 30-Dec-14 | 31-Dec-14 | 30 |
| L06-7134 | Install VCT Flooring | 2 | 2 | 30-Dec-14 | 02-Jan-15 | 20 |
| L03-8612 | L3 Pool - GWB hang/tape/finish | 6 | 6 | 31-Dec-14 | 08-Jan-15 | 13 |
| LL1-Z3-8146 | Install Restroom Accessories | 2 | 2 | 31-Dec-14 | 02-Jan-15 | 32 |

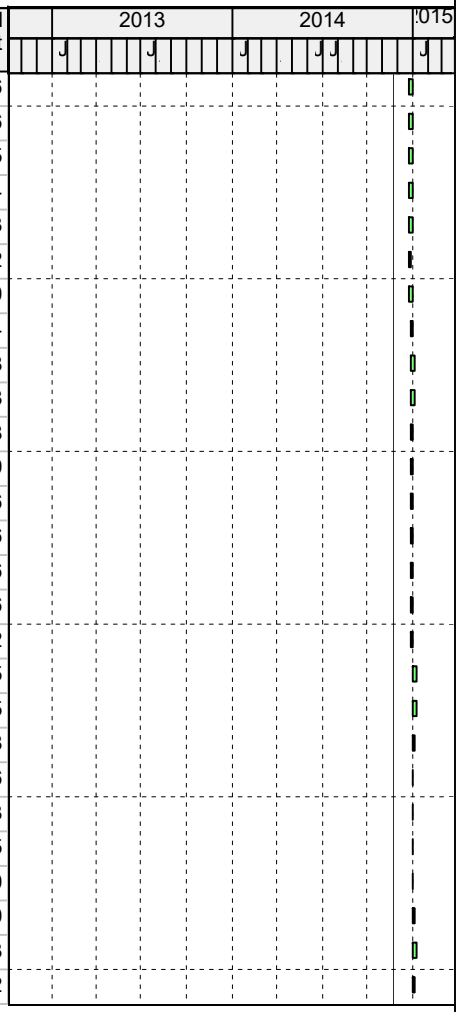



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7264 | Cx - Start-Up - Lobby Trane TRU (2) | 2 | 2 | 31-Dec-14 | 02-Jan-15 | 43 |
| CO-7132 | Cx - DDC Point-To-Point - Ballroom VAV | 1 | 1 | 31-Dec-14 | 31-Dec-14 | 35 |
| L05-7146 | Final Coat Finish Paint | 2 | 2 | 31-Dec-14 | 05-Jan-15 | 30 |
| L17-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 02-Jan-15 | 07-Jan-15 | 19 |
| L1K-8124b | Install Base | 3 | 3 | 02-Jan-15 | 06-Jan-15 | 29 |
| L17-8222 | Corridors - Fire Alarm Trim | 2 | 2 | 02-Jan-15 | 05-Jan-15 | 24 |
| CO-7244 | Cx - Heat Pump Start-Up - Levels 7 & 8 | 5 | 5 | 02-Jan-15 | 08-Jan-15 | 24 |
| CO-7134 | Cx - DDC Point-To-Point - Ballroom RTU (2) | 2 | 2 | 02-Jan-15 | 05-Jan-15 | 35 |
| SW-2048 | Zone 4 - FRP Porte Cochere drive | 5 | 5 | 02-Jan-15 | 08-Jan-15 | 39 |
| I-1620 | Enclosure at manlift - Install hat channel over framing | 4 | 4 | 02-Jan-15 | 07-Jan-15 | 30 |
| L06-7136 | Install Door and Hardware | 1 | 1 | 02-Jan-15 | 05-Jan-15 | 28 |
| L07-7134 | Install VCT Flooring | 2 | 2 | 02-Jan-15 | 06-Jan-15 | 20 |
| L1BOH2-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 05-Jan-15 | 06-Jan-15 | 25 |
| L1BOH2-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 05-Jan-15 | 06-Jan-15 | 25 |
| L1BOH2-8204 | Mech Trim / Finish (HVAC & Plumbing) | 2 | 2 | 05-Jan-15 | 06-Jan-15 | 25 |
| LL1-Z2-8118a | Install decorative light fixtures | 3 | 3 | 05-Jan-15 | 07-Jan-15 | 28 |
| CO-7228 | Cx - Start-Up - Poolpak | 1 | 1 | 05-Jan-15 | 05-Jan-15 | 43 |
| L06-7146 | Final Coat Finish Paint | 2 | 2 | 05-Jan-15 | 07-Jan-15 | 28 |
| CO-7224 | Cx - Start-Up - Gravity Relief Ventilator | 1 | 1 | 06-Jan-15 | 06-Jan-15 | 18 |
| L1K-8208 | Install Restroom Accessories | 2 | 2 | 06-Jan-15 | 07-Jan-15 | 28 |
| CO-7136 | Cx - DDC Point-To-Point - MUA AAON Start-Up (8) | 5 | 5 | 06-Jan-15 | 12-Jan-15 | 35 |
| L07-7136 | Install Door and Hardware | 1 | 1 | 06-Jan-15 | 07-Jan-15 | 26 |
| L08-7134 | Install VCT Flooring | 2 | 2 | 06-Jan-15 | 08-Jan-15 | 20 |
| L1BOH2-8201 | Final Coat Finish Paint | 5 | 5 | 07-Jan-15 | 13-Jan-15 | 25 |
| L03-8644 | L3 Pool - Connect, startup & adjust pool equipment | 10 | 10 | 07-Jan-15 | 20-Jan-15 | 35 |
| CO-7230 | Cx - TAB - Air Balancing | 15 | 15 | 07-Jan-15 | 27-Jan-15 | 18 |
| L07-7146 | Final Coat Finish Paint | 2 | 2 | 07-Jan-15 | 09-Jan-15 | 26 |

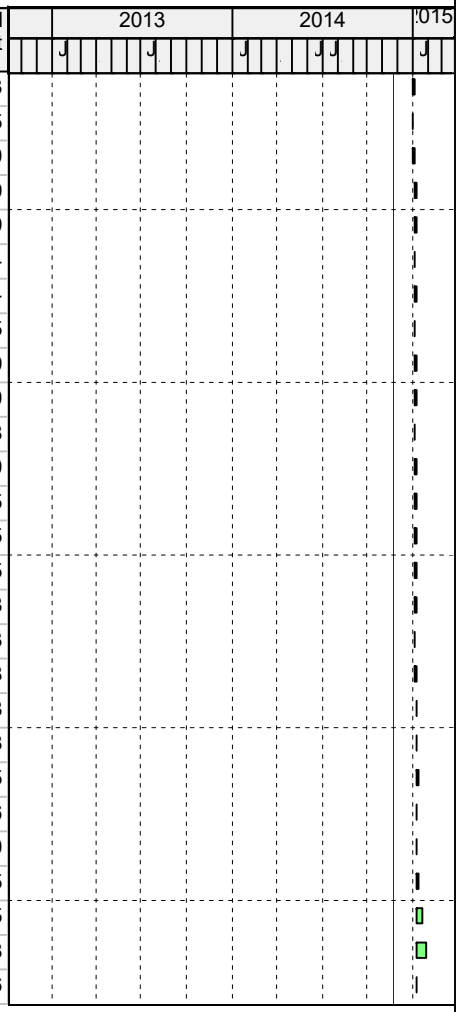



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1608 | Tower - Install N/S Wing, S. End at manlift (Elev 32) | 7 | 7 | 08-Jan-15 | 16-Jan-15 | 30 |
| MPT-1012 | Tower - Install N/S Wing, S. End E. Side Concrete (El | 7 | 7 | 08-Jan-15 | 16-Jan-15 | 38 |
| MPT-1040 | Tower - Install N/S Wing, S, End (Elev 30) | 7 | 7 | 08-Jan-15 | 16-Jan-15 | 43 |
| L03-7134 | Install VCT Flooring & Base | 2 | 2 | 08-Jan-15 | 12-Jan-15 | 21 |
| L08-7136 | Install Door and Hardware | 1 | 1 | 08-Jan-15 | 09-Jan-15 | 24 |
| L09-7134 | Install VCT Flooring | 2 | 2 | 08-Jan-15 | 12-Jan-15 | 20 |
| L11-7134 | Install VCT Flooring | 2 | 2 | 08-Jan-15 | 10-Jan-15 | 25 |
| L12-7134 | Install VCT Flooring | 2 | 2 | 08-Jan-15 | 10-Jan-15 | 25 |
| L14-7134 | Install VCT Flooring | 2 | 2 | 08-Jan-15 | 10-Jan-15 | 25 |
| L03-8614 | L3 Pool - Paint/wall finishes | 3 | 3 | 09-Jan-15 | 13-Jan-15 | 13 |
| CO-7246 | Cx - Heat Pump Start-Up - Levels 9 & 10 | 5 | 5 | 09-Jan-15 | 15-Jan-15 | 24 |
| L08-7146 | Final Coat Finish Paint | 2 | 2 | 09-Jan-15 | 13-Jan-15 | 24 |
| CO-7414 | Cx - Pressure Testing - Elevators Complete / Recall Te | 0 | 0 | | 09-Jan-15 | 31 |
| L15-7134 | Install VCT Flooring | 2 | 2 | 10-Jan-15 | 13-Jan-15 | 25 |
| L16-7134 | Install VCT Flooring | 2 | 2 | 10-Jan-15 | 13-Jan-15 | 26 |
| L17-7134 | Install VCT Flooring | 2 | 2 | 10-Jan-15 | 13-Jan-15 | 26 |
| I-3102 | Ballroom ceilings - additional work per ASIs 18, 25 | 4 | 4 | 12-Jan-15 | 15-Jan-15 | 18 |
| L1B-8120 | Install operable partitions | 3 | 3 | 12-Jan-15 | 14-Jan-15 | 19 |
| L11-7136 | Install Door and Hardware | 1 | 1 | 12-Jan-15 | 12-Jan-15 | 22 |
| L12-7136 | Install Door and Hardware | 1 | 1 | 12-Jan-15 | 12-Jan-15 | 22 |
| L14-7136 | Install Door and Hardware | 1 | 1 | 12-Jan-15 | 12-Jan-15 | 22 |
| L1B-8128 | Install Base | 2 | 2 | 12-Jan-15 | 13-Jan-15 | 20 |
| L03-7136 | Install Doors and Hardware | 2 | 2 | 12-Jan-15 | 14-Jan-15 | 21 |
| L09-7136 | Install Door and Hardware | 1 | 1 | 12-Jan-15 | 13-Jan-15 | 22 |
| L10-7134 | Install VCT Flooring | 2 | 2 | 12-Jan-15 | 14-Jan-15 | 24 |
| L1K-8128 | Install Kitchen equipment (BY OTHERS) | 5 | 5 | 13-Jan-15 | 19-Jan-15 | 15 |
| L03-8640 | L3 Pool - Prep and install plaster | 3 | 3 | 13-Jan-15 | 15-Jan-15 | 13 |

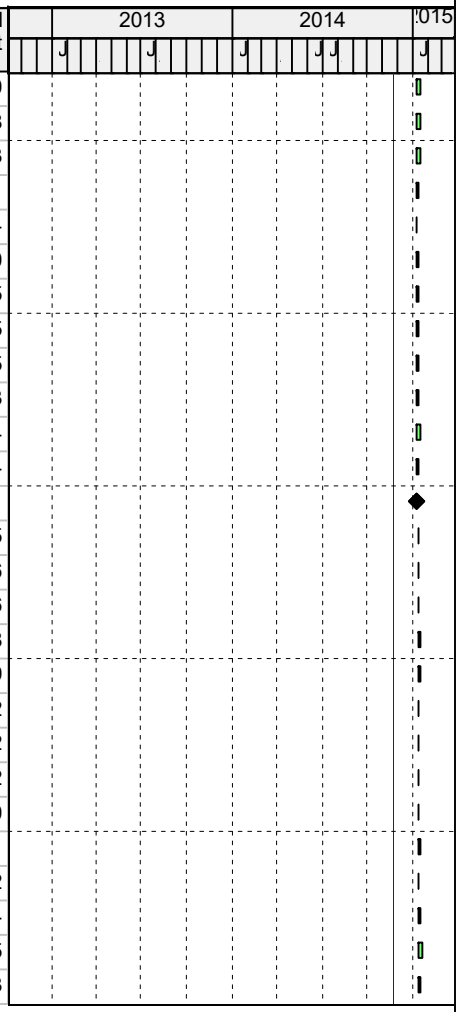



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7146 | Final Coat Finish Paint | 2 | 2 | 13-Jan-15 | 14-Jan-15 | 22 |
| L12-7146 | Final Coat Finish Paint | 2 | 2 | 13-Jan-15 | 14-Jan-15 | 22 |
| L14-7146 | Final Coat Finish Paint | 2 | 2 | 13-Jan-15 | 14-Jan-15 | 22 |
| CO-7402 | Cx - FPT - Central Plant | 2 | 2 | 13-Jan-15 | 14-Jan-15 | 35 |
| I-1206 | Concierge Lounge - Ceiling | 10 | 10 | 13-Jan-15 | 26-Jan-15 | 6 |
| L15-7136 | Install Door and Hardware | 1 | 1 | 13-Jan-15 | 14-Jan-15 | 21 |
| L16-7136 | Install Door and Hardware | 1 | 1 | 13-Jan-15 | 14-Jan-15 | 22 |
| L17-7136 | Install Door and Hardware | 1 | 1 | 13-Jan-15 | 14-Jan-15 | 22 |
| L09-7146 | Final Coat Finish Paint | 2 | 2 | 13-Jan-15 | 15-Jan-15 | 22 |
| L16-7146 | Final Coat Finish Paint | 2 | 2 | 13-Jan-15 | 15-Jan-15 | 22 |
| L17-7146 | Final Coat Finish Paint | 2 | 2 | 13-Jan-15 | 15-Jan-15 | 22 |
| L1BOH2-8134 | Clean | 4 | 4 | 14-Jan-15 | 19-Jan-15 | 25 |
| L1BOH2-8132 | Punch | 4 | 4 | 14-Jan-15 | 19-Jan-15 | 25 |
| L10-7136 | Install Door and Hardware | 1 | 1 | 14-Jan-15 | 15-Jan-15 | 20 |
| L03-7146 | Final Coat Finish Paint | 2 | 2 | 14-Jan-15 | 16-Jan-15 | 21 |
| L15-7146 | Final Coat Finish Paint | 2 | 2 | 14-Jan-15 | 16-Jan-15 | 21 |
| L03-8618 | L3 Pool - Ceramic tile at pool area | 5 | 5 | 15-Jan-15 | 21-Jan-15 | 13 |
| CO-7408 | Cx - FPT - Garage Exhaust Fans | 1 | 1 | 15-Jan-15 | 15-Jan-15 | 35 |
| L10-7146 | Final Coat Finish Paint | 2 | 2 | 15-Jan-15 | 19-Jan-15 | 20 |
| L03-8642 | L3 Pool - Fill pool | 1 | 1 | 16-Jan-15 | 16-Jan-15 | 37 |
| CO-7248 | Cx - Heat Pump Start-Up - Levels 11 & 12 | 5 | 5 | 16-Jan-15 | 22-Jan-15 | 24 |
| CO-7410 | Cx - FPT - Misc Equipment | 4 | 4 | 16-Jan-15 | 21-Jan-15 | 35 |
| I-1612 | Enclosure at manlift - Caulking | 8 | 8 | 19-Jan-15 | 28-Jan-15 | 30 |
| L1BOH2-81214 | L1, Zone 3 Complete | 0 | 0 | | 19-Jan-15 | 25 |
| CM-1024 | Tower - "Clean/Punch" Complete - All Floors | 0 | 0 | | 19-Jan-15 | 42 |
| L1K-8128a | Kitchen Equipment Final Connections | 5 | 5 | 20-Jan-15 | 26-Jan-15 | 15 |
| L03-8620 | L3 Pool - Plumbing Fixtures & Trim / Finish | 2 | 2 | 22-Jan-15 | 23-Jan-15 | 13 |

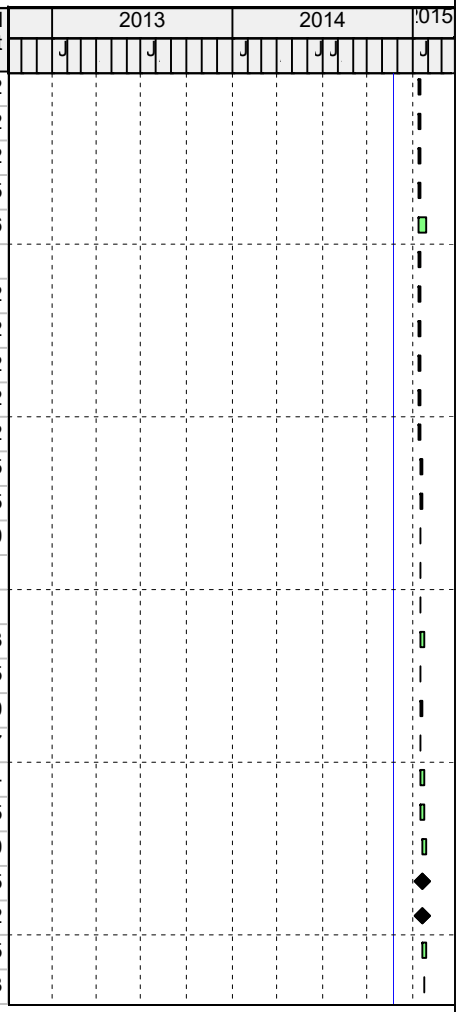



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8626 | L3 Pool - Elec Trim/ Finish | 2 | 2 | 22-Jan-15 | 23-Jan-15 | 13 |
| L03-8628 | L3 Pool - Elec Specialties Trim / Finish | 2 | 2 | 22-Jan-15 | 23-Jan-15 | 13 |
| L03-8630 | L3 Pool - Doors & Hardware | 2 | 2 | 22-Jan-15 | 23-Jan-15 | 13 |
| L03-8638 | L3 Pool - Install pool deck and ADA lift | 3 | 3 | 22-Jan-15 | 26-Jan-15 | 31 |
| CO-7250 | Cx - Heat Pump Start-Up - Levels 14 & 15 | 5 | 5 | 23-Jan-15 | 29-Jan-15 | 24 |
| CO-7404 | Cx - FPT - Heat Pumps | 3 | 3 | 23-Jan-15 | 27-Jan-15 | 31 |
| L03-8632 | L3 Pool - Install Bathroom Accessories | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 13 |
| CO-7406 | Cx - FPT - MUA, RTU, VAV and Exhaust Fans | 5 | 5 | 26-Jan-15 | 30-Jan-15 | 18 |
| L03-8646 | L3 Pool - Health inspections | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 30 |
| CO-7218 | Cx - Heat Pump Start-Up - Levels 16 & 17 | 5 | 5 | 30-Jan-15 | 05-Feb-15 | 24 |
| L1L-8124a | Install Base | 3 | 3 | 02-Feb-15 | 04-Feb-15 | 4 |
| I-1202 | Concierge Lounge - Additional flooring work | 3 | 3 | 03-Feb-15 | 05-Feb-15 | 1 |
| L1L-8120 | Install plumbing at bar | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 4 |
| L1L-8122 | Install electrical at bar | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 4 |
| CO-7118T | City of Bellevue/3rd Party Fire Alarm Inspection / Appl | 5 | 5 | 05-Feb-15 | 11-Feb-15 | 20 |
| I-1204 | Concierge Lounge - Additional millwork | 4 | 4 | 06-Feb-15 | 11-Feb-15 | 0 |
| CO-7112T | City of Bellevue/3rd Party Fire Sprinkler Inspection / A | 5 | 5 | 12-Feb-15 | 18-Feb-15 | 15 |
| CO-7106T | City of Bellevue/3rd Party Smoke Control Testing (Tow | 5 | 5 | 12-Feb-15 | 18-Feb-15 | 15 |
| CM-1022 | Podium - "Clean/Punch" Complete - All Floors, All Zon | 0 | 0 | | 23-Feb-15 | 17 |
| CO-7412 | Cx - Pressure Testing - GC Indicates Building Comple | 0 | 0 | | 23-Feb-15* | 0 |
| CO-7416 | Cx - Pressure Testing - Pre-Walk with GC | 1 | 1 | 24-Feb-15 | 24-Feb-15 | 0 |
| CO-7418 | Cx - Pressure Testing - GC Makes Corrections | 5 | 5 | 24-Feb-15 | 02-Mar-15 | 0 |
| CO-7420 | Cx - Pressure Testing - Pressure Pre-Test | 2 | 2 | 03-Mar-15 | 04-Mar-15 | 0 |
| CO-7422 | Cx - Pressure Testing -Corrections | 2 | 2 | 05-Mar-15 | 06-Mar-15 | 0 |
| CO-7424 | Cx - Pressure Testing - Pressure Final Test | 1 | 1 | 09-Mar-15 | 09-Mar-15 | 0 |
| CO-7426 | Cx - Pressure Testing - Building Final Corrections | 2 | 2 | 10-Mar-15 | 11-Mar-15 | 0 |
| CO-7124 | Complete Final Building Inspections | 5 | 5 | 12-Mar-15 | 18-Mar-15 | 0 |

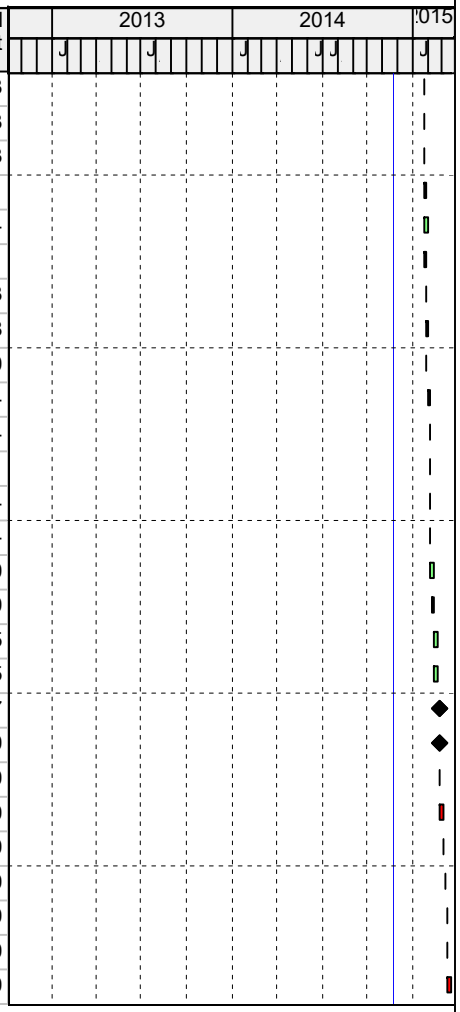



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13 A | | |
| CM-1002 | CM - Contract Time (578 Cal Days) | 576 | 0 | 06-Mar-13 A | 05-Oct-14 A | |
| CM-1014 | CM - Start of Construction | 0 | 0 | 05-Apr-13 A | | |
| CM-1006 | Construction Documents Issued by Client - (Due on 7 | 0 | 0 | 24-Nov-14 | | 115 |
| CO-7004 | CO - Prep / Submit O&M Manuals | 40 | 40 | 24-Nov-14 | 02-Jan-15 | 75 |
| CM-1008 | Finalization of Allowances - (Due on 9-2-13) | 0 | 0 | 24-Nov-14 | | 115 |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 08-Dec-14* | | 29 |
| CM-1016 | CM - Owner FF+E "Build-Out" - Floors 4-10 | 14 | 14 | 08-Dec-14 | 22-Dec-14 | 29 |
| CM-1018 | CM - Hotel Operations Training | 21 | 21 | 22-Dec-14 | 12-Jan-15 | 66 |
| CO-7006 | CO - Certificate of Occupancy/Substantial Completior | 0 | 0 | | 18-Mar-15 | 0 |
| CO-7122 | CO - Certificate of Occupancy | 0 | 0 | | 18-Mar-15 | 0 |
| **Misc Milestones** | | | | | | |
| CM-1020 | MM - Site Mobilization | 10 | 0 | 06-Mar-13 A | 04-Apr-13 A | |
| MM-1008 | MM - Top Out - Tower / Structure | 0 | 0 | | 16-Apr-14 A | |
| MM-1004 | MM - Start Drywall In Tower | 0 | 0 | 27-Jun-14 A | | |
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 06-Sep-14 A | |
| MM-1010 | Energize Permanent Power | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| **Tower Crane** | | | | | | |
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 0 | 04-Jun-13 A | 14-Jun-13 A | |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 0 | 20-Jun-13 A | 24-Jun-13 A | |
| TC-5902 | Tower Crane - Erectiion | 2 | 0 | 21-Jun-13 A | 24-Jun-13 A | |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 24-Jun-13 A | | |

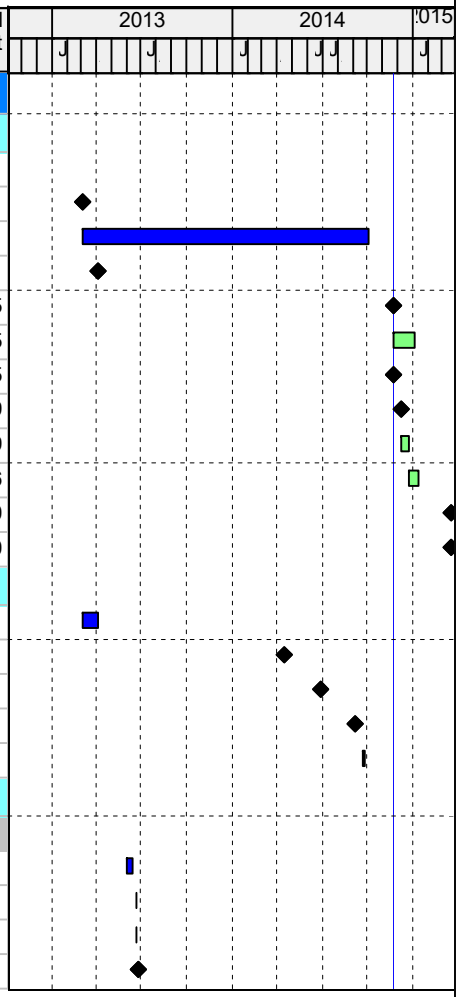


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| TC-5906 | Tower Crane - Operatational Period | 391 | 0 | 24-Jun-13 A | 16-Jun-14 A | |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 0 | 16-Jun-14 A | 17-Jun-14 A | |
| **Man & Material Lifts** | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 0 | 14-Jan-14 A | 20-Jan-14 A | |
| ML-5952 | Man/Material Lifts - Erect/Build Loading Dock | 5 | 0 | 21-Jan-14 A | 27-Jan-14 A | |
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 10-Feb-14 A | | |
| ML-5954 | Man/Material Lifts - Load Test / Certify | 1 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| ML-5958 | Man/Material Lifts - Operatational Period | 196 | 0 | 10-Feb-14 A | 15-Nov-14 A | |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 2 | 0 | 15-Nov-14 A | 16-Nov-14 A | |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |
| **Mass Excavation / Shoring** | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 0 | 05-Apr-13 A | 12-Apr-13 A | |
| SW-2002 | Demolition And Utility Relocation | 8 | 0 | 15-Apr-13 A | 19-Apr-13 A | |
| SW-2010 | Grade Subgrade for Elect/Plumbing | 3 | 0 | 07-Jan-14 A | 09-Jan-14 A | |
| **Site Finishes** | | | | | | |
| SW-2006 | Install Perm Power Electrical Service / Dry Utilities (Ofl | 15 | 0 | 20-May-14 A | 05-Jun-14 A | |
| SW-2004 | Offsite Water & Water Connection | 9 | 0 | 22-Sep-14 A | 01-Oct-14 A | |
| SW-2008 | Zone 4 - Landscaping & irrigation | 5 | 5 | 09-Jan-15 | 15-Jan-15 | 39 |
| **Structure** | | | | | | |
| **Foundation / Substructure - (Levels LL4 / LL3)** | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 0 | 12-Jun-13 A | 27-Jun-13 A | |
| LL4-1601 | LL4 - Excavate Footings | 14 | 0 | 17-Jun-13 A | 30-Jul-13 A | |
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 0 | 18-Jun-13 A | 24-Jun-13 A | |
| LL4-1606 | LL4 - Undrgmd Plumbing | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |

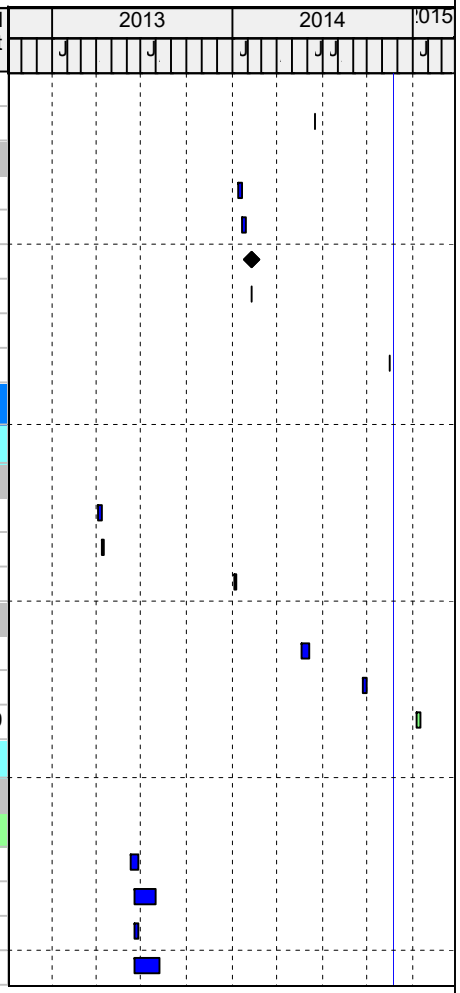



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-1608 | LL4 - Undrgrnd Elec | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 0 | 19-Jun-13 A | 25-Jun-13 A | |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 0 | 26-Jun-13 A | 02-Aug-13 A | |
| LL4-2033 | LL4 - Shotcrete Walls | 27 | 0 | 26-Jun-13 A | 05-Aug-13 A | |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 0 | 03-Jul-13 A | 21-Aug-13 A | |
| LL4-1614 | LL4 - FRP SOG | 5 | 0 | 10-Jul-13 A | 07-Aug-13 A | |
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 0 | 12-Jul-13 A | 26-Jul-13 A | |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 0 | 13-Jul-13 A | 06-Aug-13 A | |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 0 | 22-Jul-13 A | 24-Jul-13 A | |
| LL4-1618 | LL4 - FRP Ramp SOG | 5 | 0 | 01-Aug-13 A | 07-Aug-13 A | |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2004 | LL2 - Shore / Form Deck | 8 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2006 | LL3 - M & E Inserts | 4 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2008 | LL3 - ReSteel / PT Cables | 6 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2010 | LL3 - Install Embeds | 2 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2001 | LL3 - Waterproof Walls | 3 | 0 | 05-Aug-13 A | 05-Aug-13 A | |
| LL3-2012 | LL3 - Pour / Finish Deck | 2 | 0 | 16-Aug-13 A | 16-Aug-13 A | |
| LL3-2014 | LL3 - Stress Tendons | 1 | 0 | 19-Aug-13 A | 19-Aug-13 A | |
| LL3-2000 | LL3 - FRP Core Walls | 8 | 0 | 19-Aug-13 A | 28-Aug-13 A | |
| LL3-2033 | LL3 - Shotcrete Walls | 5 | 0 | 23-Aug-13 A | 26-Aug-13 A | |
| LL3-2016 | LL3 - Strip / ReShore Deck | 3 | 0 | 01-Sep-13 A | 13-Sep-13 A | |
| LL3-2018 | LL3 - Remove ReShores | 4 | 0 | 04-Nov-13 A | 07-Nov-13 A | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Grids 1 to 4 - (SOG @ Loading Dock)** | | | | | | |
| LL2-2056 | LL2 - Grease Intercepter | 5 | 0 | 15-Aug-13 A | 21-Aug-13 A | |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 0 | 27-Aug-13 A | 04-Sep-13 A | |

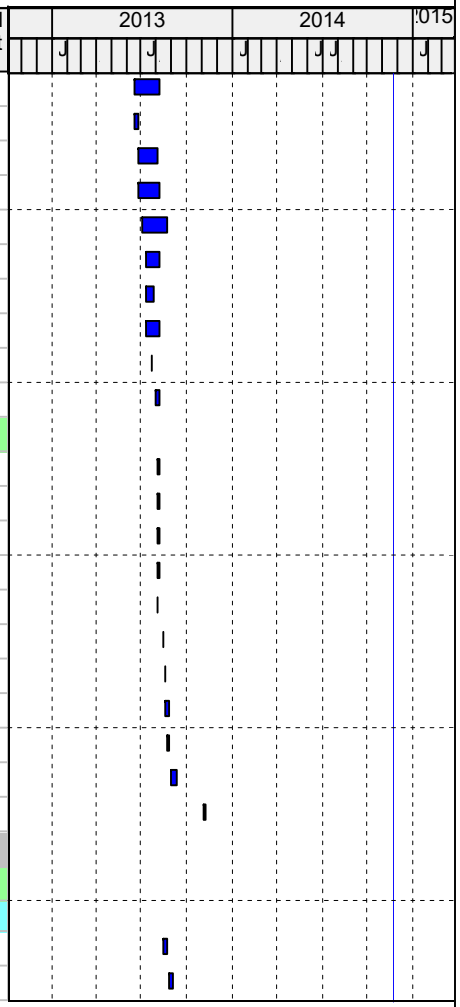



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2027 | LL2 - Waterproof Walls | 2 | 0 | 27-Aug-13 A | 28-Aug-13 A | |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 0 | 30-Aug-13 A | 05-Sep-13 A | |
| LL2-2021 | LL2 - FRP Elec Vault | 14 | 0 | 30-Aug-13 A | 04-Sep-13 A | |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 0 | 04-Sep-13 A | 11-Sep-13 A | |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 0 | 11-Sep-13 A | 13-Sep-13 A | |
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls/Roof | 11 | 0 | 19-Sep-13 A | 03-Oct-13 A | |
| LL2-2020 | LL2 - Undrgmd Plumbing | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2022 | LL2 - Undrgmd Elec | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2031 | LL2 - FRP Generator SOG | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2015 | LL2 to LL1 FRP Columns / Misc Walls | 6 | 0 | 01-Oct-13 A | 01-Oct-13 A | |
| LL2-2029 | LL2 - F/R/P Pour #2 | 8 | 0 | 15-Jan-14 A | 24-Jan-14 A | |
| LL2-2011 | LL2 - F/R/P Pour #3 | 16 | 0 | 24-Jan-14 A | 18-Feb-14 A | |
| LL2-2019 | LL2 - F/R/P Pour #6 | 4 | 0 | 19-Feb-14 A | 17-Mar-14 A | |
| LL2-2044 | LL2 - Set Generator | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |
| LL2-2004 | LL2 - Shore / Form Deck | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2035 | LL2 to LL1 - Shotcrete Walls | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2006 | LL2 - M & E Inserts | 4 | 0 | 14-Aug-13 A | 19-Aug-13 A | |
| LL2-2008 | LL2 - ReSteel / PT Cables | 6 | 0 | 14-Aug-13 A | 21-Aug-13 A | |
| LL2-2010 | LL2 - Install Embeds | 3 | 0 | 14-Aug-13 A | 16-Aug-13 A | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 0 | 27-Aug-13 A | 06-Sep-13 A | |
| LL2-2012 | LL2 - Place / Finish Deck | 3 | 0 | 29-Aug-13 A | 29-Aug-13 A | |
| LL2-2023 | LL2 - Waterproof Walls | 3 | 0 | 29-Aug-13 A | 03-Sep-13 A | |
| LL2-2014 | LL2 - Stress Tendons | 1 | 0 | 30-Aug-13 A | 30-Aug-13 A | |
| LL2-2016 | LL2 - Strip / ReShore | 3 | 0 | 03-Sep-13 A | 05-Sep-13 A | |
| LL2-8234 | LL2 - Place / Finish Deck | 3 | 0 | 12-Sep-13 A | 12-Sep-13 A | |

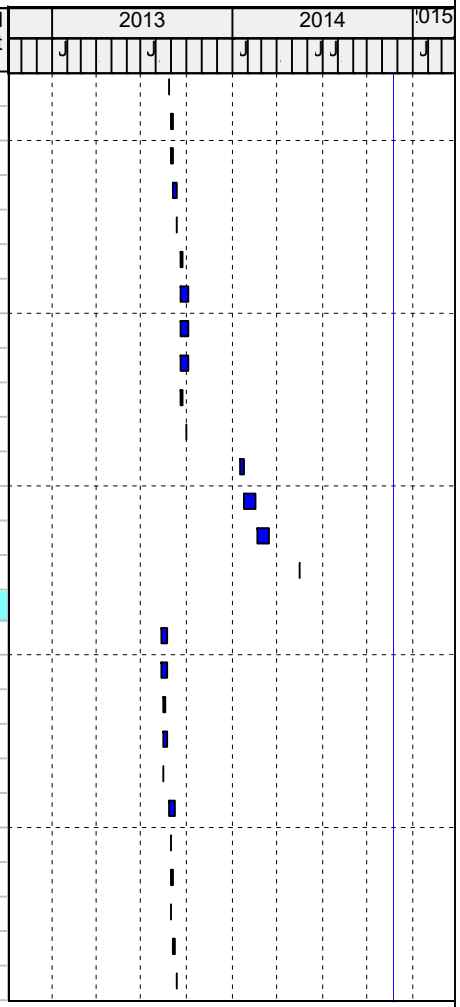


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2000 | LL2 - FRP Core Walls | 8 | 0 | 12-Sep-13 A | 23-Sep-13 A | |
| LL2-2018 | LL2 - Remove ReShores | 4 | 0 | 13-Nov-13 A | 18-Nov-13 A | |
| LL2-2013 | LL2 - F/R/P Pour #1 | 4 | 0 | 13-Jan-14 A | 16-Jan-14 A | |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| P5A-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2000 | LL1 - FRP Core Walls | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2004 | LL1 - Shore / Form Deck | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| P6-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P6-2004 | LL1 - Shore / Form Deck | 7 | 0 | 16-Sep-13 A | 24-Sep-13 A | |
| P5A-2006 | LL1 - MEP Rough In | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2008 | LL1 - ReSteel / PT Cables | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2012 | LL1 - Place / Finish Deck | 0 | 0 | 20-Sep-13 A | | |
| P5A-2020 | LL1 - Waterproof Walls | 3 | 0 | 20-Sep-13 A | 24-Sep-13 A | |
| P5A-2014 | LL1 - Stress Tendons | 1 | 0 | 23-Sep-13 A | 23-Sep-13 A | |
| P5A-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2006 | LL1 - MEP Rough In | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2008 | LL1 - ReSteel / PT Cables | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 24-Sep-13 A | 25-Sep-13 A | |
| P6-2020 | LL1 - Waterproof Walls | 4 | 0 | 24-Sep-13 A | 27-Sep-13 A | |
| P5A-2033 | LL1 - Resteel/Shotcrete Walls | 3 | 0 | 25-Sep-13 A | 27-Sep-13 A | |
| P5B-2002 | LL1 - FRP Columns Below | 5 | 0 | 26-Sep-13 A | 02-Oct-13 A | |
| P5B-2004 | LL1 - Shore / Form Deck | 7 | 0 | 26-Sep-13 A | 04-Oct-13 A | |
| P6-2012 | LL1 - Place / Finish Deck | 0 | 0 | 27-Sep-13 A | | |
| P6-2014 | LL1 - Stress Tendons | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2033 | LL1 - Resteel/Shotcrete Walls | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 01-Oct-13 A | 03-Oct-13 A | |

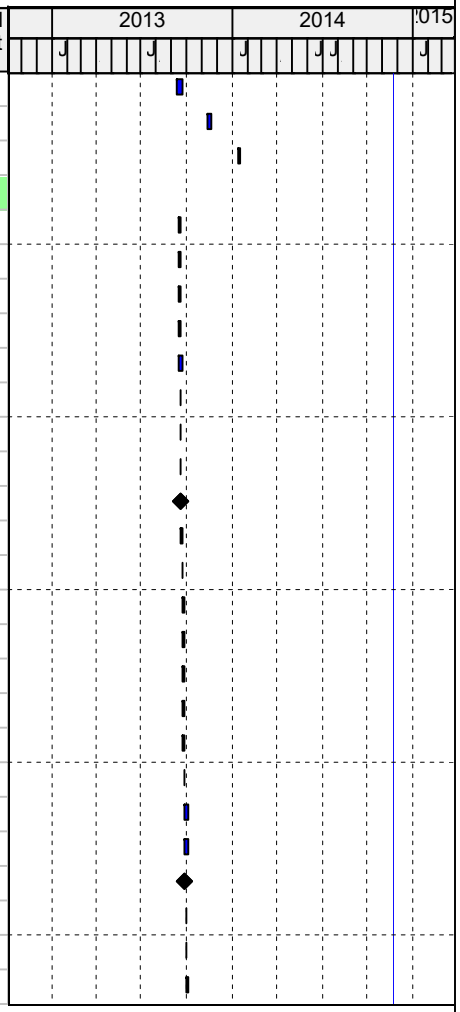


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P5B-2006 | LL1 - MEP Rough In | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2002 | FRP Columns Below | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2004 | Shore / Form Deck | 4 | 0 | 03-Oct-13 A | 08-Oct-13 A | |
| P5B-2008 | LL1 - ReSteel / PT Cables | 5 | 0 | 04-Oct-13 A | 10-Oct-13 A | |
| P5B-2010 | LL1 - Install Edgeform/Embeds | 4 | 0 | 04-Oct-13 A | 09-Oct-13 A | |
| P8-2002 | FRP Columns Below | 5 | 0 | 07-Oct-13 A | 11-Oct-13 A | |
| P8-2000 | Form/Resteel/Close Core Walls | 14 | 0 | 07-Oct-13 A | 24-Oct-13 A | |
| P8-2004 | Shore / Form Deck P8 | 8 | 0 | 07-Oct-13 A | 16-Oct-13 A | |
| P7-2002 | FRP Columns Below | 5 | 0 | 08-Oct-13 A | 14-Oct-13 A | |
| P7-2004 | Shore / Form Deck | 6 | 0 | 08-Oct-13 A | 15-Oct-13 A | |
| P10A--2006 | MEP Rough In | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2008 | ReSteel / PT Cables | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2010 | Install Edgeform/Embeds | 2 | 0 | 08-Oct-13 A | 09-Oct-13 A | |
| P5B-2012 | LL1 - Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P10A--2012 | Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P5B-2014 | LL1 - Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P7-2006 | MEP Rough In | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P7-2008 | ReSteel / PT Cables | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P10A--2014 | Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P8-2020 | Shore / Form Deck P9 | 6 | 0 | 14-Oct-13 A | 21-Oct-13 A | |
| P5B-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2010 | Install Edgeform/Embeds | 2 | 0 | 15-Oct-13 A | 16-Oct-13 A | |
| P8-2006 | MEP Rough In | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2008 | ReSteel / PT Cables | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2010 | Install Edgeform/Embeds | 4 | 0 | 15-Oct-13 A | 18-Oct-13 A | |
| P10A--2016 | Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2012 | Place / Finish Deck | 0 | 0 | 18-Oct-13 A | | |

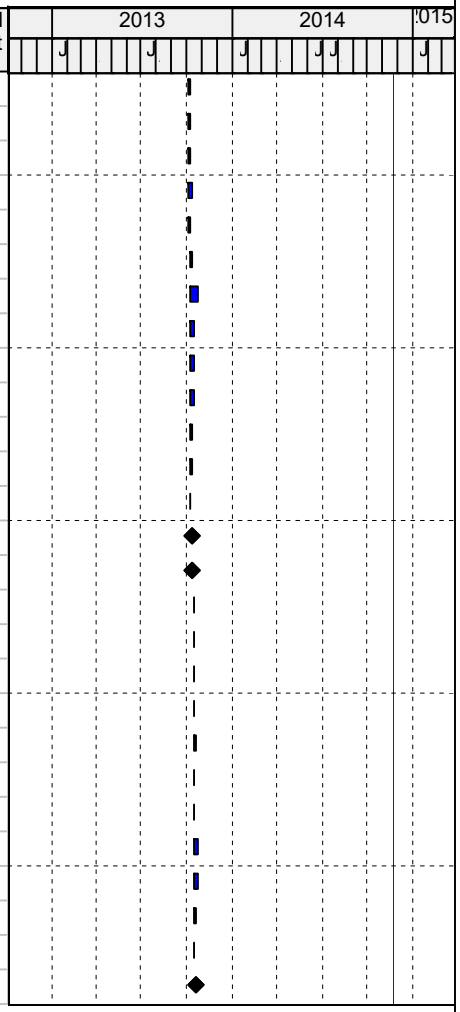



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P7-2033 | Resteel/Shotcrete Walls | 3 | 0 | 18-Oct-13 A | 22-Oct-13 A | |
| P7-2014 | Stress Tendons | 1 | 0 | 21-Oct-13 A | 21-Oct-13 A | |
| P7-2016 | Strip / ReShore Deck | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2002 | FRP Columns Below | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P10B--2000 | FRP Shear Walls Below | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2004 | Shore / Form Deck | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P8-2012 | Place / Finish Deck P 8 & 9 and Core Walls | 0 | 0 | 25-Oct-13 A | | |
| P8-2014 | Stress Tendons | 1 | 0 | 28-Oct-13 A | 28-Oct-13 A | |
| P10B--2006 | MEP Rough In | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2008 | ReSteel / PT Cables | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2010 | Install Edgeform/Embeds | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P12--2002 | FRP Columns Below | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P12--2000 | Form/Resteel/Close Core Walls | 9 | 0 | 28-Oct-13 A | 07-Nov-13 A | |
| P12--2004 | Shore / Form Deck | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P8-2016 | Strip / ReShore Deck | 3 | 0 | 29-Oct-13 A | 31-Oct-13 A | |
| P11--2002 | FRP Columns Below | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P11--2004 | Shore / Form Deck | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P10B--2012 | Place / Finish Deck | 0 | 0 | 31-Oct-13 A | | |
| P10B--2014 | Stress Tendons | 1 | 0 | 01-Nov-13 A | 01-Nov-13 A | |
| P12--2006 | MEP Rough In | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12--2008 | ReSteel / PT Cables | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12--2010 | Install Edgeform/Embeds | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P10B--2016 | Strip / ReShore Deck | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2006 | MEP Rough In | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2008 | ReSteel / PT Cables | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2010 | Install Edgeform/Embeds | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2012 | Place / Finish Deck | 0 | 0 | 07-Nov-13 A | | |

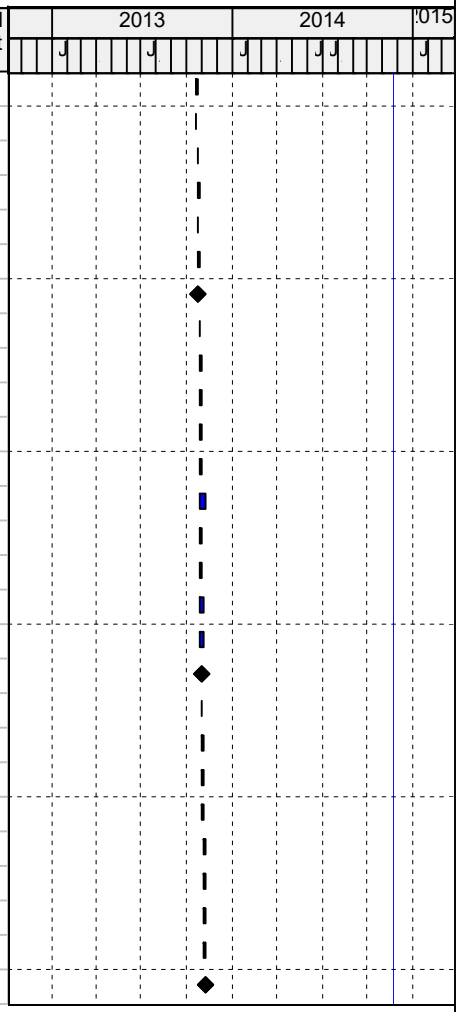


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P13–2002 | FRP Columns Below | 5 | 0 | 07-Nov-13 A | 14-Nov-13 A | |
| P13–2004 | Shore / Form Deck | 9 | 0 | 07-Nov-13 A | 28-Nov-13 A | |
| P11–2014 | Stress Tendons | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| P12–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 08-Nov-13 A | | |
| P11–2016 | Strip / ReShore Deck | 3 | 0 | 12-Nov-13 A | 14-Nov-13 A | |
| P12–2014 | Stress Tendons | 1 | 0 | 12-Nov-13 A | 12-Nov-13 A | |
| P14–2002 | FRP Columns Below | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P14–2000 | Form/Resteel/Close Core Walls | 8 | 0 | 19-Nov-13 A | 03-Dec-13 A | |
| P14–2004 | Shore / Form Deck | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P13A–2002 | FRP Columns Below | 5 | 0 | 21-Nov-13 A | 27-Nov-13 A | |
| P13A–2004 | Shore / Form Deck | 4 | 0 | 21-Nov-13 A | 26-Nov-13 A | |
| P13–2010 | Install Edgeform/Embeds | 5 | 0 | 22-Nov-13 A | 04-Dec-13 A | |
| P13–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2006 | MEP Rough In | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2010 | Install Edgeform/Embeds | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P13–2006 | MEP Rough In | 5 | 0 | 26-Nov-13 A | 03-Dec-13 A | |
| P13A–2006 | MEP Rough In | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2008 | ReSteel / PT Cables | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2010 | Install Edgeform/Embeds | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13–2012 | Place / Finish Deck | 0 | 0 | 02-Dec-13 A | | |
| P13A–2012 | Place / Finish Deck | 0 | 0 | 03-Dec-13 A | | |
| P14–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 04-Dec-13 A | | |
| P13–2014 | Stress Tendons | 1 | 0 | 05-Dec-13 A | 05-Dec-13 A | |
| P15–2002 | FRP Columns Below | 3 | 0 | 05-Dec-13 A | 09-Dec-13 A | |
| P15–2000 | Jump/Resteel/Close Core | 9 | 0 | 05-Dec-13 A | 17-Dec-13 A | |
| P15–2004 | Shore / Form Deck | 5 | 0 | 05-Dec-13 A | 11-Dec-13 A | |

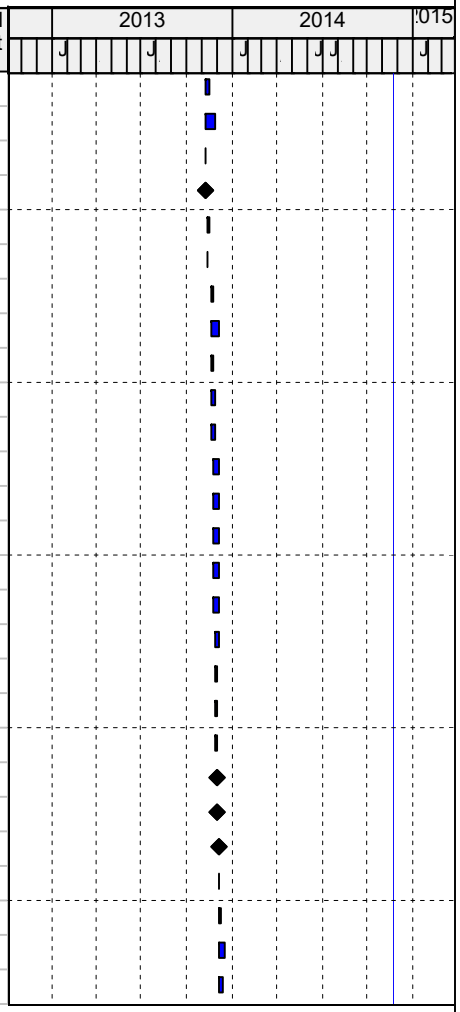



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P13–2016 | Strip / ReShore Deck | 3 | 0 | 06-Dec-13 A | 10-Dec-13 A | |
| P13A–2014 | Stress Tendons | 1 | 0 | 06-Dec-13 A | 06-Dec-13 A | |
| P14–2014 | Stress Tendons | 1 | 0 | 07-Dec-13 A | 07-Dec-13 A | |
| P15–2006 | MEP Rough In | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2008 | ReSteel / PT Cables | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2010 | Install Edgeform/Embeds | 3 | 0 | 11-Dec-13 A | 13-Dec-13 A | |
| P16-2002 | FRP Columns Below | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P16-2004 | Shore / Form Deck | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P15–2012 | Place / Finish Deck | 0 | 0 | 18-Dec-13 A | | |
| P15–2020 | Place Conc @ Core | 0 | 0 | 18-Dec-13 A | | |
| P16-2000 | Jump/Resteel/Close Core | 5 | 0 | 18-Dec-13 A | 24-Dec-13 A | |
| P16-2006 | MEP Rough In | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2008 | ReSteel / PT Cables | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2010 | Install Edgeform/Embeds | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P15–2014 | Stress Tendons | 1 | 0 | 21-Dec-13 A | 21-Dec-13 A | |
| P8-2018 | Remove Reshores | 2 | 0 | 23-Dec-13 A | 24-Dec-13 A | |
| P10A–2018 | Remove Reshores | 2 | 0 | 26-Dec-13 A | 27-Dec-13 A | |
| P16-2012 | Place / Finish Deck | 0 | 0 | 26-Dec-13 A | | |
| P16-2020 | Place Conc @ Core | 0 | 0 | 26-Dec-13 A | | |
| P17-2002 | FRP Columns Below | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P17-2000 | Jump/Resteel/Close Core | 7 | 0 | 27-Dec-13 A | 07-Jan-14 A | |
| P17-2004 | Shore / Form Deck | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P10B–2018 | Remove Reshores | 2 | 0 | 30-Dec-13 A | 31-Dec-13 A | |
| P16-2014 | Stress Tendons | 1 | 0 | 31-Dec-13 A | 31-Dec-13 A | |
| P5A-2018 | LL1 - Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P11–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P12–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |

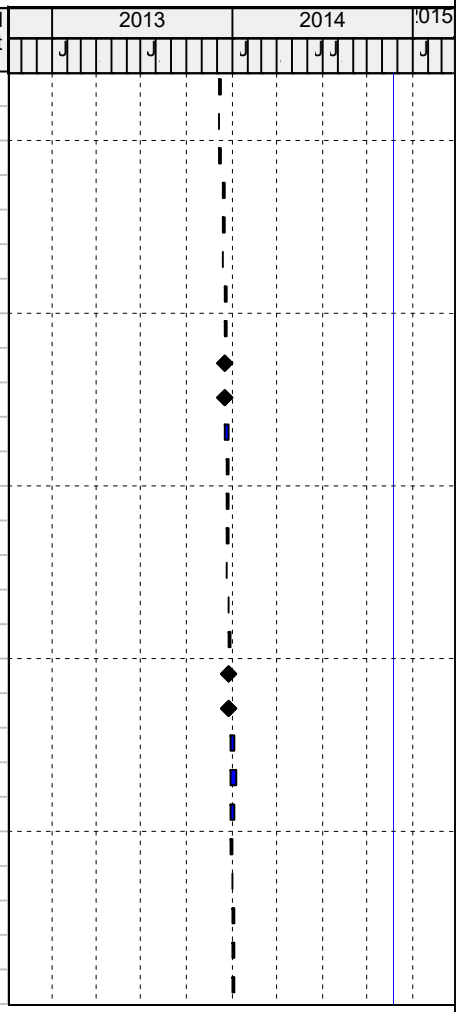


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P17-2006 | MEP Rough In | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2008 | ReSteel / PT Cables | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2010 | Install Edgeform/Embeds | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P6-2018 | LL1 - Remove Reshores | 2 | 0 | 06-Jan-14 A | 07-Jan-14 A | |
| P5B-2018 | LL1 - Remove Reshores | 2 | 0 | 08-Jan-14 A | 09-Jan-14 A | |
| P17-2012 | Place / Finish Deck | 0 | 0 | 08-Jan-14 A | | |
| P17-2020 | Place Conc @ Core | 0 | 0 | 08-Jan-14 A | | |
| P18-2002 | FRP Columns Below | 5 | 0 | 09-Jan-14 A | 15-Jan-14 A | |
| P18-2000 | Jump/Resteel/Close Core | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P18-2004 | Shore / Form Deck | 3 | 0 | 09-Jan-14 A | 13-Jan-14 A | |
| LL2-2022R | MEP Rough In | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P7-2018 | Remove Reshores | 2 | 0 | 10-Jan-14 A | 13-Jan-14 A | |
| P17-2014 | Stress Tendons | 1 | 0 | 11-Jan-14 A | 11-Jan-14 A | |
| P13–2018 | Remove Reshores | 2 | 0 | 13-Jan-14 A | 14-Jan-14 A | |
| P13A–2018 | Remove Reshores | 2 | 0 | 15-Jan-14 A | 16-Jan-14 A | |
| WEA-2012 | WIND IMPACT | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| P18-2006 | MEP Rough In | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2008 | ReSteel / PT Cables | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2010 | Install Edgeform/Embeds | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2012 | Place / Finish Deck | 0 | 0 | 22-Jan-14 A | | |
| P18-2020 | Place Conc @ Core | 0 | 0 | 22-Jan-14 A | | |
| P19-2002 | FRP Columns Below | 5 | 0 | 23-Jan-14 A | 29-Jan-14 A | |
| P19-2000 | Jump/Resteel/Close Core | 4 | 0 | 23-Jan-14 A | 28-Jan-14 A | |
| P19-2004 | Shore / Form Deck | 3 | 0 | 23-Jan-14 A | 27-Jan-14 A | |
| P18-2014 | Stress Tendons | 1 | 0 | 25-Jan-14 A | 25-Jan-14 A | |
| P14–2018 | Remove Reshores | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2006 | MEP Rough In | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |

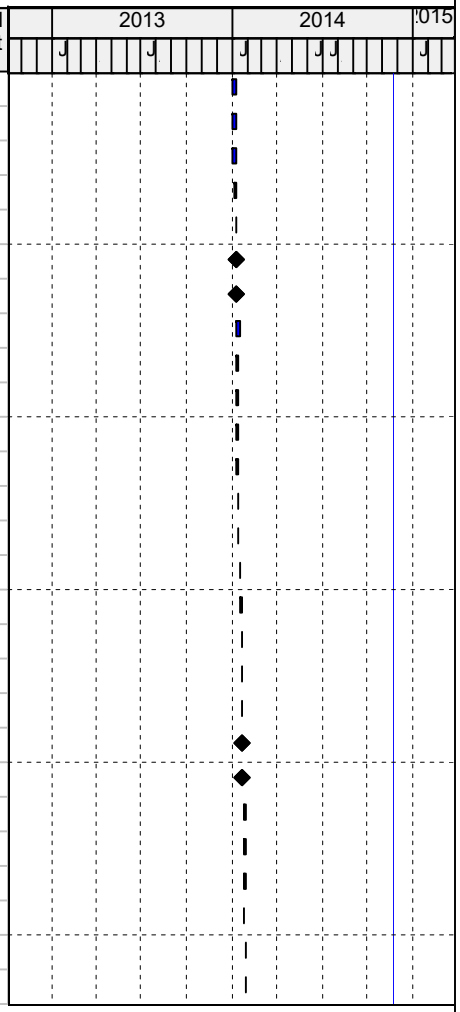



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P19-2008 | ReSteel / PT Cables | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2010 | Install Edgeform/Embeds | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2012 | Place / Finish Deck | 0 | 0 | 29-Jan-14 A | | |
| P19-2020 | Place Conc @ Core | 0 | 0 | 29-Jan-14 A | | |
| P20-2002 | FRP Columns Below | 5 | 0 | 30-Jan-14 A | 05-Feb-14 A | |
| P20-2000 | Jump/Resteel/Close Core | 9 | 0 | 30-Jan-14 A | 11-Feb-14 A | |
| P20-2004 | Shore / Form Deck | 6 | 0 | 30-Jan-14 A | 10-Feb-14 A | |
| P19-2014 | Stress Tendons | 1 | 0 | 01-Feb-14 A | 01-Feb-14 A | |
| P13A–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P14–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P15–2016 | Strip / ReShore Deck | 3 | 0 | 06-Feb-14 A | 10-Feb-14 A | |
| P20-2006 | MEP Rough In | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2008 | ReSteel / PT Cables | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2010 | Install Edgeform/Embeds | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| L03-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 06-Feb-14 A | 12-Feb-14 A | |
| P16-2016 | Strip / ReShore Deck | 3 | 0 | 10-Feb-14 A | 12-Feb-14 A | |
| L04-2018 | Remove Reshores | 2 | 0 | 10-Feb-14 A | 11-Feb-14 A | |
| L03-2018 | Remove Reshores | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| P17-2016 | Strip / ReShore Deck | 3 | 0 | 12-Feb-14 A | 14-Feb-14 A | |
| P20-2012 | Place / Finish Deck | 0 | 0 | 12-Feb-14 A | | |
| P20-2020 | Place Conc @ Core | 0 | 0 | 12-Feb-14 A | | |
| L04-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-Feb-14 A | 18-Feb-14 A | |
| P12–2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P18-2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P21-2002 | FRP Columns Below | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| P21-2000 | Jump/Resteel/Close Core | 4 | 0 | 13-Feb-14 A | 18-Feb-14 A | |
| P21-2004 | Shore / Form Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |

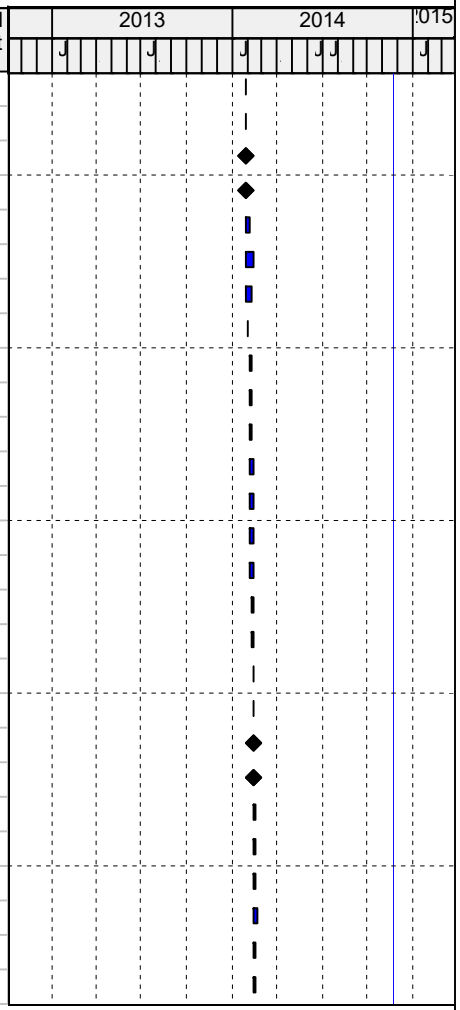


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P19-2016 | Strip / ReShore Deck | 3 | 0 | 14-Feb-14 A | 18-Feb-14 A | |
| P20-2014 | Stress Tendons | 1 | 0 | 15-Feb-14 A | 15-Feb-14 A | |
| P21-2006 | MEP Rough In | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2008 | ReSteel / PT Cables | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P20-2016 | Strip / ReShore Deck | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| L05-2018 | Remove Reshores | 2 | 0 | 18-Feb-14 A | 19-Feb-14 A | |
| P21-2012 | Place / Finish Deck | 0 | 0 | 19-Feb-14 A | | |
| P21-2020 | Place Conc @ Core | 0 | 0 | 19-Feb-14 A | | |
| P22-2002 | FRP Columns Below | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P22-2000 | Jump/Resteel/Close Core | 4 | 0 | 20-Feb-14 A | 25-Feb-14 A | |
| P22-2004 | Shore / Form Deck | 3 | 0 | 20-Feb-14 A | 24-Feb-14 A | |
| L05-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P21-2014 | Stress Tendons | 1 | 0 | 22-Feb-14 A | 22-Feb-14 A | |
| P21-2016 | Strip / ReShore Deck | 3 | 0 | 24-Feb-14 A | 26-Feb-14 A | |
| P22-2006 | MEP Rough In | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2008 | ReSteel / PT Cables | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| L06-2018 | Remove Reshores | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| P22-2012 | Place / Finish Deck | 0 | 0 | 26-Feb-14 A | | |
| P22-2020 | Place Conc @ Core | 0 | 0 | 26-Feb-14 A | | |
| P23-2002 | FRP Columns Below | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2000 | Jump/Resteel/Close Core | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2004 | Shore / Form Deck | 3 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2006 | MEP Rough In | 2 | 0 | 01-Mar-14 A | 03-Mar-14 A | |
| P22-2014 | Stress Tendons | 1 | 0 | 01-Mar-14 A | 01-Mar-14 A | |
| P23-2008 | ReSteel / PT Cables | 2 | 0 | 03-Mar-14 A | 04-Mar-14 A | |

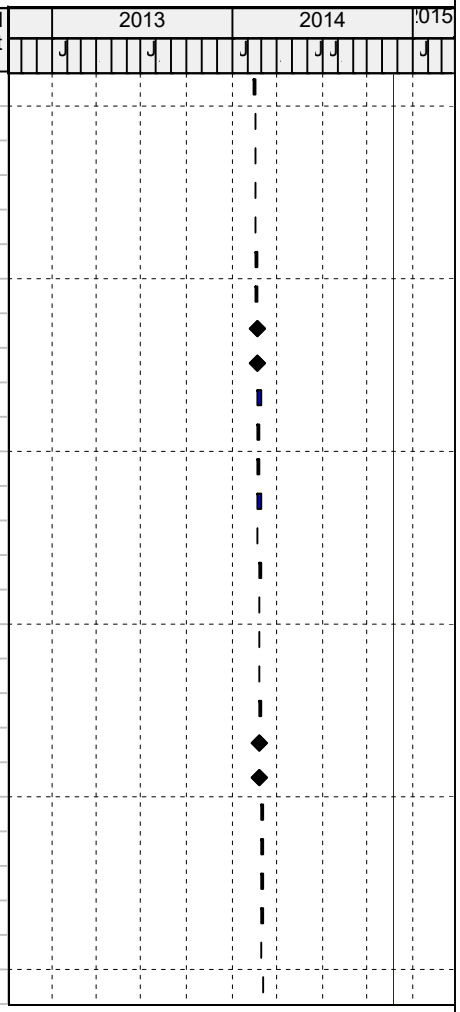



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P22-2016 | Strip / ReShore Deck | 3 | 0 | 04-Mar-14 A | 10-Mar-14 A | |
| P23-2010 | Install Edgeform/Embeds | 2 | 0 | 04-Mar-14 A | 04-Mar-14 A | |
| L07-2018 | Remove Reshores | 2 | 0 | 04-Mar-14 A | 05-Mar-14 A | |
| P23-2012 | Place / Finish Deck | 0 | 0 | 05-Mar-14 A | | |
| P23-2020 | Place Conc @ Core | 0 | 0 | 05-Mar-14 A | | |
| P24-2002 | FRP Columns Below | 5 | 0 | 05-Mar-14 A | 07-Mar-14 A | |
| P24-2004 | Shore / Form Deck | 3 | 0 | 06-Mar-14 A | 10-Mar-14 A | |
| P24-2000 | Jump/Resteel/Close Core | 4 | 0 | 08-Mar-14 A | 10-Mar-14 A | |
| P23-2014 | Stress Tendons | 1 | 0 | 10-Mar-14 A | 10-Mar-14 A | |
| P24-2008 | ReSteel / PT Cables | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P24-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P23-2016 | Strip / ReShore Deck | 3 | 0 | 11-Mar-14 A | 17-Mar-14 A | |
| P24-2006 | MEP Rough In | 2 | 0 | 11-Mar-14 A | 11-Mar-14 A | |
| P25-2002 | FRP Columns Below | 5 | 0 | 11-Mar-14 A | 13-Mar-14 A | |
| L08-2018 | Remove Reshores | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| P24-2012 | Place / Finish Deck | 0 | 0 | 12-Mar-14 A | | |
| P24-2020 | Place Conc @ Core | 0 | 0 | 12-Mar-14 A | | |
| P25-2004 | Shore / Form Deck | 3 | 0 | 13-Mar-14 A | 17-Mar-14 A | |
| P25-2000 | Jump/Resteel/Close Core | 4 | 0 | 15-Mar-14 A | 17-Mar-14 A | |
| P24-2014 | Stress Tendons | 1 | 0 | 17-Mar-14 A | 17-Mar-14 A | |
| P25-2006 | MEP Rough In | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2008 | ReSteel / PT Cables | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| L06-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 18-Mar-14 A | 20-Mar-14 A | |
| L09-2018 | Remove Reshores | 2 | 0 | 18-Mar-14 A | 19-Mar-14 A | |
| P26-2002 | FRP Columns Below | 5 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| P25-2012 | Place / Finish Deck | 0 | 0 | 19-Mar-14 A | | |

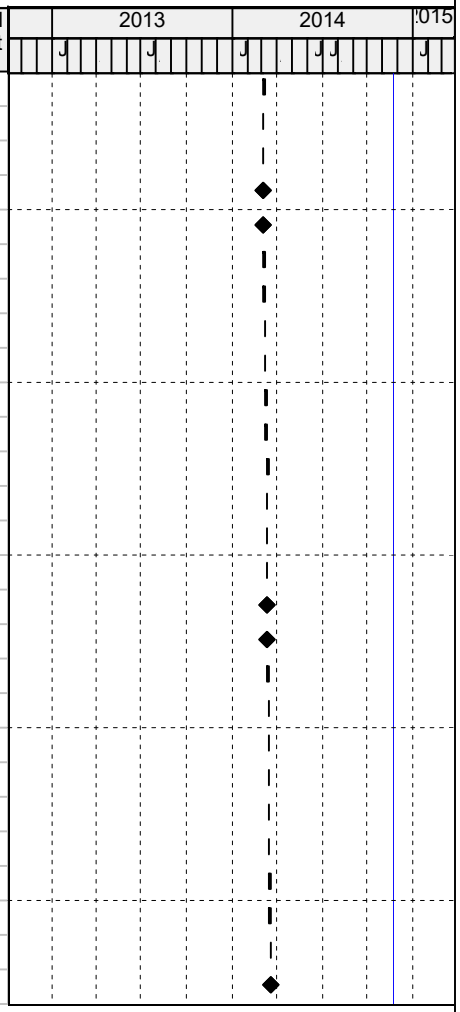



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P25-2020 | Place Conc @ Core | 0 | 0 | 19-Mar-14 A | | |
| P26-2004 | Shore / Form Deck | 3 | 0 | 20-Mar-14 A | 24-Mar-14 A | |
| L07-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 21-Mar-14 A | 25-Mar-14 A | |
| P26-2000 | Jump/Resteel/Close Core | 4 | 0 | 22-Mar-14 A | 24-Mar-14 A | |
| P26-2006 | MEP Rough In | 2 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P26-2008 | ReSteel / PT Cables | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P26-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P25-2014 | Stress Tendons | 1 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P27-2002 | FRP Columns Below | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| P26-2012 | Place / Finish Deck | 0 | 0 | 26-Mar-14 A | | |
| P26-2020 | Place Conc @ Core | 0 | 0 | 26-Mar-14 A | | |
| L08-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 26-Mar-14 A | 28-Mar-14 A | |
| L10-2018 | Remove Reshores | 2 | 0 | 26-Mar-14 A | 27-Mar-14 A | |
| P27-2004 | Shore / Form Deck | 3 | 0 | 27-Mar-14 A | 31-Mar-14 A | |
| P27-2000 | Jump/Resteel/Close Core | 4 | 0 | 29-Mar-14 A | 31-Mar-14 A | |
| P27-2006 | MEP Rough In | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2008 | ReSteel / PT Cables | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2010 | Install Edgeform/Embeds | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P26-2014 | Stress Tendons | 1 | 0 | 31-Mar-14 A | 31-Mar-14 A | |
| L09-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 31-Mar-14 A | 02-Apr-14 A | |
| P24-2016 | Strip / ReShore Deck | 3 | 0 | 01-Apr-14 A | 07-Apr-14 A | |
| L11-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 02-Apr-14 A | |
| L12-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 03-Apr-14 A | |
| P27-2012 | Place / Finish Deck | 0 | 0 | 02-Apr-14 A | | |
| P27-2020 | Place Conc @ Core | 0 | 0 | 02-Apr-14 A | | |
| P28-2002 | FRP Columns Below | 5 | 0 | 02-Apr-14 A | 04-Apr-14 A | |
| P28-2004 | Shore / Form Deck | 4 | 0 | 03-Apr-14 A | 08-Apr-14 A | |

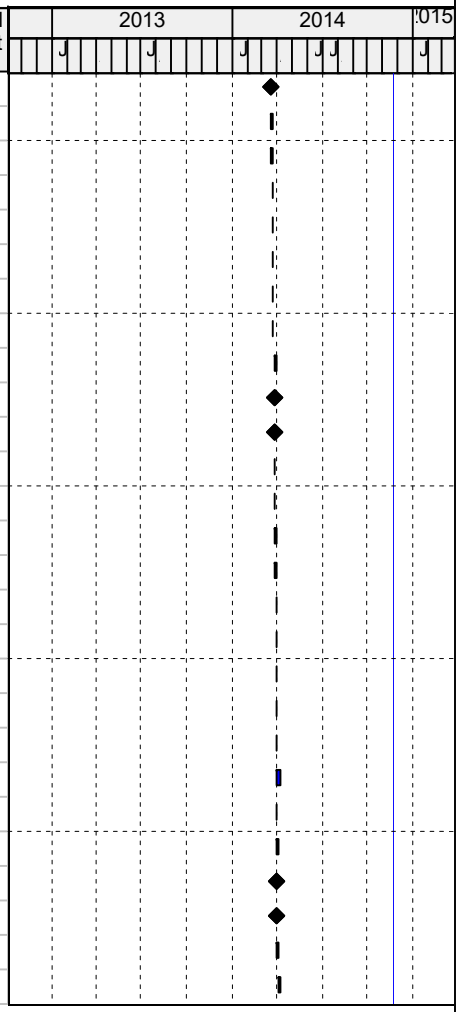


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| P27-2014 | Stress Tendons | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| P25-2016 | Strip / ReShore Deck | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L14-2018 | Remove Reshores | 2 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| P28-2000 | Jump/Resteel/Close Core | 7 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| P28-2006 | MEP Rough In | 4 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2008 | ReSteel / PT Cables | 4 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Apr-14 A | 11-Apr-14 A | |
| L12-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| P28-2012 | Place / Finish Deck | 0 | 0 | 14-Apr-14 A | | |
| P28-2020 | Place Conc @ Core | 0 | 0 | 14-Apr-14 A | | |
| P29-2002 | FRP Columns Above Roof Deck | 3 | 0 | 14-Apr-14 A | 18-Apr-14 A | |
| P26-2016 | Strip / ReShore Deck | 3 | 0 | 14-Apr-14 A | 17-Apr-14 A | |
| L14-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-Apr-14 A | 18-Apr-14 A | |
| P28-2014 | Stress Tendons | 1 | 0 | 17-Apr-14 A | 17-Apr-14 A | |
| P29-2000 | Strip Core | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| P27-2016 | Strip / ReShore Deck | 3 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L15-2018 | Remove Reshores | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| P28-2016 | Strip / ReShore Deck | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L15-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L16-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-May-14 A | 19-May-14 A | |
| L16-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2019 | Grind Ceiling for Skim Coat | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| **Ballroom Catwalk & Roof** | | | | | | |
| PC-2100 | Erect Structural Steel @ Porte Cochere | 3 | 0 | 30-Jan-14 A | 03-Feb-14 A | |

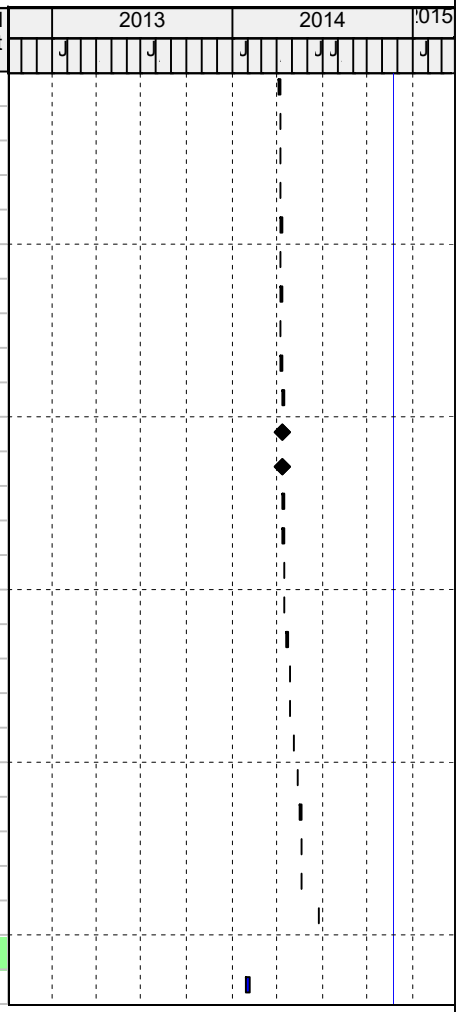


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 7 | 0 | 07-Feb-14 A | 17-Feb-14 A | |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| PC-2102 | Metal Decking @ Porte Cochere/ Roof | 2 | 0 | 17-Apr-14 A | 18-Apr-14 A | |
| BR-2112 | BR - Fireproofing @ Structural Steel | 2 | 0 | 27-May-14 A | 30-May-14 A | |
| Upper Tower - (Levels 3 thru PH) | | | | | | |
| **Mech Penthouse** | | | | | | |
| PH-8706 | Set Mech Equipment @ Tower Roof | 3 | 0 | 22-May-14 A | 28-May-14 A | |
| PH-8708 | Set Equipment @ Penthouse | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| PH-8700 | PH - Structural Steel and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| **Vertical Circulation** | | | | | | |
| Stairs | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 25-Nov-13 A | 26-Nov-13 A | |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 27-Nov-13 A | 03-Dec-13 A | |
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 04-Dec-13 A | 05-Dec-13 A | |
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 06-Dec-13 A | 09-Dec-13 A | |
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 2 | 0 | 03-Feb-14 A | 04-Feb-14 A | |
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 2 | 0 | 06-Feb-14 A | 07-Feb-14 A | |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 2 | 0 | 07-Feb-14 A | 07-Feb-14 A | |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 2 | 0 | 07-Feb-14 A | 10-Feb-14 A | |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 2 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 2 | 0 | 06-Mar-14 A | 07-Mar-14 A | |
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 2 | 0 | 07-Mar-14 A | 10-Mar-14 A | |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |

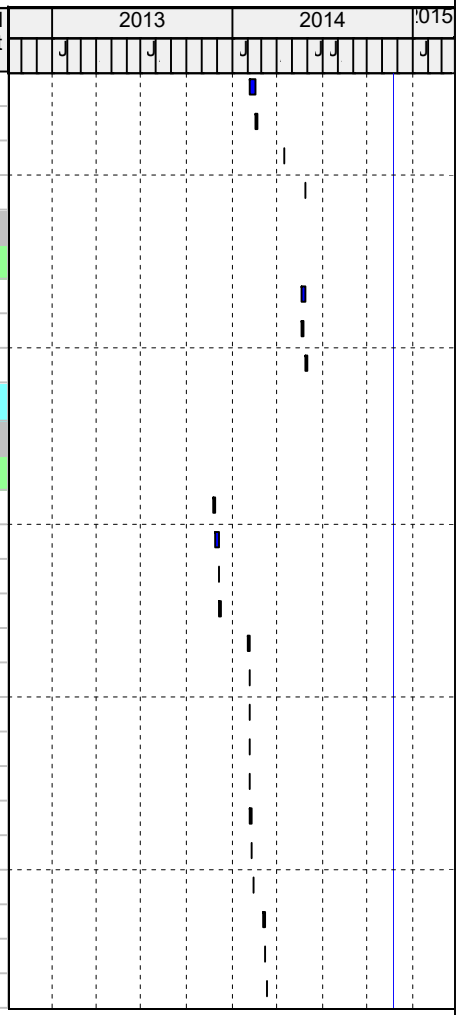



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 2 | 0 | 13-Mar-14 A | 14-Mar-14 A | |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 2 | 0 | 08-Apr-14 A | 21-Apr-14 A | |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| S1-4040 | Stair 1 - Set Mtl Stairs / Railings L18 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 10-Dec-13 A | 11-Dec-13 A | |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 12-Dec-13 A | 13-Dec-13 A | |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 16-Dec-13 A | 17-Dec-13 A | |
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 18-Dec-13 A | 19-Dec-13 A | |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 2 | 0 | 12-Feb-14 A | 13-Feb-14 A | |
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 2 | 0 | 13-Feb-14 A | 13-Feb-14 A | |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 2 | 0 | 13-Feb-14 A | 14-Feb-14 A | |
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 2 | 0 | 19-Feb-14 A | 20-Feb-14 A | |
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 2 | 0 | 21-Feb-14 A | 24-Feb-14 A | |
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 2 | 0 | 19-Mar-14 A | 20-Mar-14 A | |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 2 | 0 | 21-Mar-14 A | 22-Mar-14 A | |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 2 | 0 | 14-May-14 A | 15-May-14 A | |
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 2 | 0 | 16-May-14 A | 19-May-14 A | |
| S2-4038 | Stair 2 - Set Mtl Stairs / Railings L17 | 2 | 0 | 19-May-14 A | 20-May-14 A | |

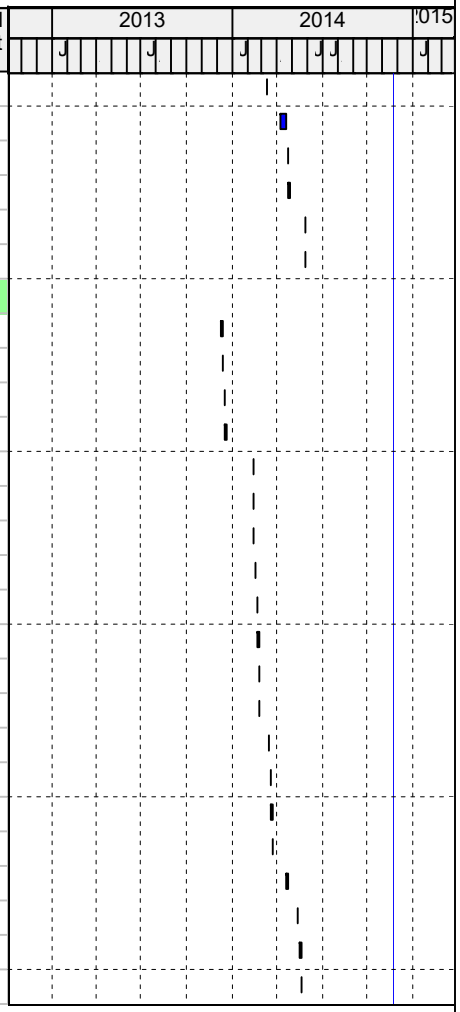



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - Set Metal Stairs / Railings LL2 | 6 | 0 | 05-Mar-14 A | 20-Mar-14 A | |
| S3-4002 | Stair 3 - Set Metal Stairs / Railings LL1 | 6 | 0 | 17-Mar-14 A | 21-Mar-14 A | |
| S3-4004 | Stair 3 - Permanent Railings / Final Finishes | 4 | 4 | 02-Jan-15 | 07-Jan-15 | 40 |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |
| S4-4000 | Stair 4 - Set Metal Stairs / Railings LL2 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4002 | Stair 4 - Set Metal Stairs / Railings LL1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4004 | Stair 4 -Set Metal Stairs / Railings L1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4006 | Stair 4 - Permanent Railings / Final Finishes | 4 | 4 | 14-Jan-15 | 19-Jan-15 | 30 |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |
| S6-4000 | Stair 6 - Set Metal Stairs / Railings | 5 | 0 | 25-Jun-14 A | 01-Jul-14 A | |
| S6-4002 | Stair 6 - Permanent Railings / Final Finishes | 2 | 2 | 31-Dec-14 | 02-Jan-15 | 43 |
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes | 5 | 5 | 03-Feb-15 | 09-Feb-15 | 17 |
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a -Set Metal Stairs / Railings L1 | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| S4a-4002 | Stair 4a - Permanent Railings / Final Finishes | 2 | 2 | 20-Jan-15 | 21-Jan-15 | 30 |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 07-Jun-13 A | | |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 0 | 17-Jun-13 A | 21-Jun-13 A | |
| EL-1004 | Elev - Submittal Approval | 21 | 0 | 21-Jun-13 A | 01-Jan-14 A | |
| EL-1006 | Elev - Release to Manufacturing | 14 | 0 | 02-Jan-14 A | 15-Jan-14 A | |
| EL-1008 | Elev - Fabrication (Engineered Geared) | 95 | 0 | 16-Jan-14 A | 14-Jun-14 A | |
| EL-1010 | Elev - Machines delivered | 1 | 0 | 12-May-14 A | 12-May-14 A | |

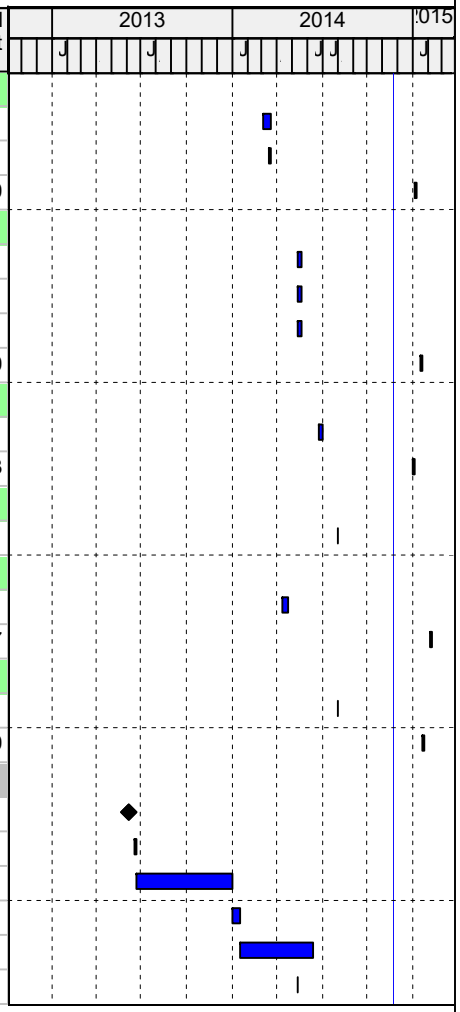


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-1011 | Elev - Elevator Machines Flown & Set At Top Of Hoist | 5 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5016 | Elev 5 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-1216 | Elev 1&2 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-3416 | Elev 3&4 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-1202 | Elev 1&2 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-3402 | Elev 3&4 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-5018 | Elev 5 - Set Hoistway Machines | 3 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| EL-1218 | Elev 1&2 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-3418 | Elev 3&4 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-1200 | Elev 1&2 - Hoistway Clear & Ready (GC) | 0 | 0 | 20-Jun-14 A | | |
| EL-1204 | Elev 1&2 - Install Rails & Brackets | 17 | 0 | 23-Jun-14 A | 15-Jul-14 A | |
| EL-3400 | Elev 3&4 - Hoistway Clear & Ready (GC) | 0 | 0 | 23-Jun-14 A | | |
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 24-Jun-14 A | | |
| EL-1206 | Elev 1&2 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Jul-14 A | |
| EL-1207 | Elev 1&2 - Install Pit Equipment/Car Sling/CWT Fram | 3 | 0 | 15-Jul-14 A | 01-Aug-14 A | |
| EL-1208 | Elev 1&2 - Install MHoist & Cable | 5 | 0 | 16-Jul-14 A | 24-Jul-14 A | |
| EL-3407 | Elev 3&4 - Install Pit Equipment/Car Sling/CWT Fram | 5 | 0 | 16-Jul-14 A | 06-Aug-14 A | |
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 21-Jul-14 A | | |
| EL-5004 | Elev 5 - Install Rails & Brackets | 13 | 0 | 21-Jul-14 A | 11-Aug-14 A | |
| EL-3404 | Elev 3&4 - Install Rails & Brackets | 18 | 0 | 23-Jul-14 A | 04-Aug-14 A | |
| EL-3406 | Elev 3&4 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 28-Jul-14 A | |
| EL-3408 | Elev 3&4 - Install Hoist & Cable | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| EL-5007 | Elev 5 - Install Pit Equipment/Car Sling/CWT Frame/V | 5 | 0 | 12-Aug-14 A | 15-Aug-14 A | |
| EL-1210 | Elev 1&2 - Install Entrances/Doors/Fixtures/Fascia | 19 | 0 | 14-Aug-14 A | 22-Sep-14 A | |
| EL-3410 | Elev 3&4 - Install Entrances/Doors/Fixtures/Fascia | 30 | 0 | 14-Aug-14 A | 02-Oct-14 A | |

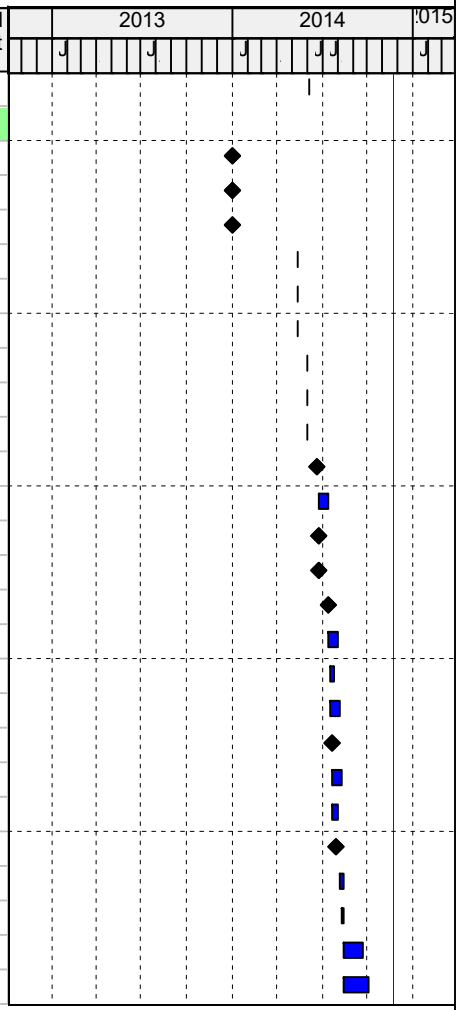


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-5006 | Elev 5 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Aug-14 A | |
| EL-5008 | Elev 5 - Install MHoist & Cable | 4 | 0 | 18-Aug-14 A | 20-Aug-14 A | |
| EL-5010 | Elev 5 - Install Entrances/Doors/Fixtures/Fascia | 21 | 0 | 21-Aug-14 A | 26-Sep-14 A | |
| EL-1212 | Elev 1&2 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 22-Sep-14 A | 13-Oct-14 A | |
| EL-5012 | Elev 5 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 26-Sep-14 A | 16-Oct-14 A | |
| EL-3412 | Elev 3&4 - Install Hoistway Equipment/Pipe & Wire | 23 | 0 | 03-Oct-14 A | 03-Nov-14 A | |
| EL-1214 | Elev 1&2 - Install Cab/Wiring/Door Operator(s) | 11 | 0 | 14-Oct-14 A | 28-Oct-14 A | |
| EL-5014 | Elev 5 - Install Cab/Wiring/Door Operator(s) | 7 | 0 | 17-Oct-14 A | 27-Oct-14 A | |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 1 | 0 | 24-Oct-14 A | 24-Oct-14 A | |
| EL-6016 | Elev 6 - Hoistway Walls Complete (GC) | 0 | 0 | | 24-Oct-14 A | |
| EL-6004 | Elev 6 - Install Cylinders/Rails & Brackets | 4 | 0 | 27-Oct-14 A | 30-Oct-14 A | |
| EL-5022 | Elev 5 - Adjust | 5 | 0 | 28-Oct-14 A | 03-Nov-14 A | |
| EL-1222 | Elev 1&2 - Adjust | 5 | 0 | 29-Oct-14 A | 04-Nov-14 A | |
| EL-6006 | Elev 6 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 30-Oct-14 A | |
| EL-6007 | Elev 6 - Install Pit Equipment/Car Sling | 2 | 0 | 31-Oct-14 A | 03-Nov-14 A | |
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| EL-3414 | Elev 3&4 - Install Cab/Wiring/Door Operator(s) | 10 | 0 | 04-Nov-14 A | 17-Nov-14 A | |
| EL-6018 | Elev 6 - Install Machine Room Equipment | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| EL-1224 | Elev 1&2 - Clean / Paint / Punchlist | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| EL-5026 | Elev 5 - Inspections | 7 | 0 | 13-Nov-14 A | 14-Nov-14 A | |
| EL-3422 | Elev 3&4 - Adjust | 8 | 0 | 18-Nov-14 A | 20-Nov-14 A | |
| EL-6012 | Elev 6 - Install hoistway rails & divider beams | 2 | 0 | 20-Nov-14 A | 21-Nov-14 A | |
| EL-3424 | Elev 3&4 - Walsh/TKE pre-inspection | 6 | 6 | 01-Dec-14 | 08-Dec-14 | 47 |
| EL-6010 | Elev 6 - Install elevator fronts/rears | 9 | 9 | 08-Dec-14 | 18-Dec-14 | 27 |
| EL-6014 | Elev 6 - Cab build-out | 5 | 5 | 08-Dec-14 | 12-Dec-14 | 26 |
| EL-1226 | Elev 1&2 - CoB/L&I Inspections | 5 | 5 | 09-Dec-14* | 15-Dec-14 | 47 |
| EL-3426 | Elev 3&4 - Inspections | 5 | 5 | 09-Dec-14 | 15-Dec-14 | 47 |

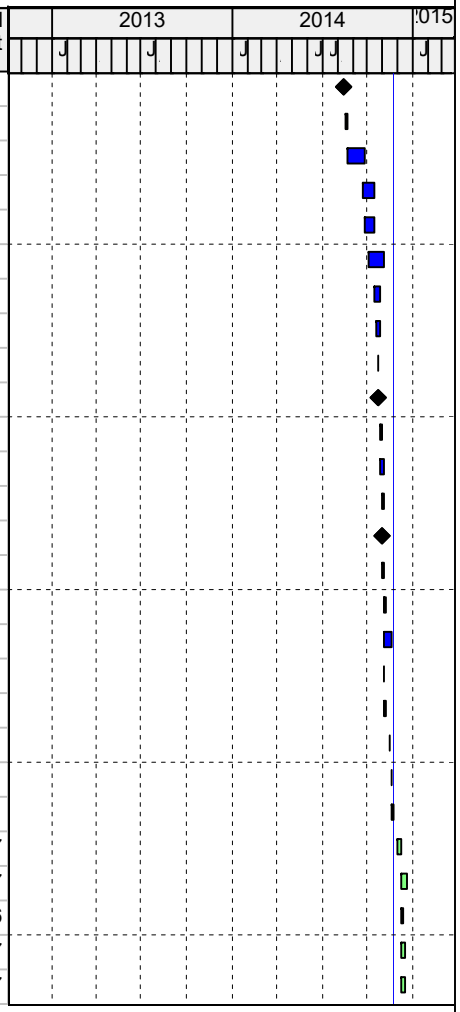


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6022 | Elev 6 - Final cleaning at EMR | 4 | 4 | 31-Dec-14 | 06-Jan-15 | 26 |
| EL-6024 | Elev 6 - Walsh/TKE pre-inspection | 2 | 2 | 07-Jan-15 | 08-Jan-15 | 26 |
| EL-6026 | Elev 6 - CoB/L&I Inspections | 1 | 1 | 09-Jan-15 | 09-Jan-15 | 26 |
| **Exterior Shell** | | | | | | |
| **Elevations** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2** | | | | | | |
| L3D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Feb-14 A | 12-Feb-14 A | |
| L3-5308 | L3- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 17-Feb-14 A | 21-Feb-14 A | |
| L4D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Feb-14 A | 19-Feb-14 A | |
| L4-5308 | L4- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Feb-14 A | 28-Feb-14 A | |
| L5D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Feb-14 A | 26-Feb-14 A | |
| L5-5308 | L5- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 03-Mar-14 A | 07-Mar-14 A | |
| L6D5308 | Deliver/Stock Wall Panels | 1 | 0 | 05-Mar-14 A | 05-Mar-14 A | |
| L6-5308 | L6- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L7-5308 | L7- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L7D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Mar-14 A | 12-Mar-14 A | |
| L8D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Mar-14 A | 19-Mar-14 A | |
| L8-5308 | L8- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Mar-14 A | 28-Mar-14 A | |
| L9D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L9-5308 | L9- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 31-Mar-14 A | 07-Apr-14 A | |
| 10D5308 | Deliver/Stock Wall Panels | 1 | 0 | 02-Apr-14 A | 02-Apr-14 A | |
| L10-5308 | L10- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 07-Apr-14 A | 11-Apr-14 A | |
| 11D5308 | Deliver/Stock Wall Panels | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L11-5308 | L11- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 11-Apr-14 A | 18-Apr-14 A | |
| 12D5308 | Deliver/Stock Wall Panels | 1 | 0 | 16-Apr-14 A | 16-Apr-14 A | |
| L12-5308 | L12- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Apr-14 A | 25-Apr-14 A | |

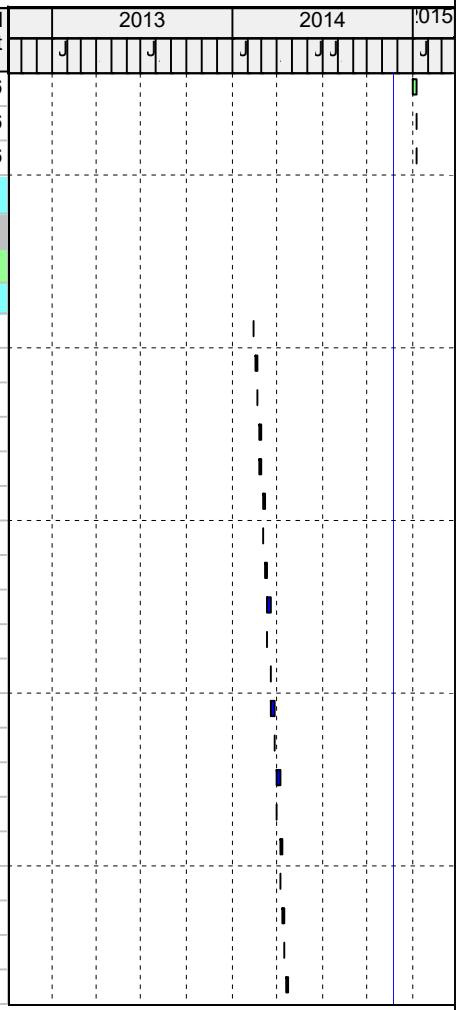



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| 14D5308 | Deliver/Stock Wall Panels | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L14-5308 | L14 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Apr-14 A | 01-May-14 A | |
| 15D5308 | Deliver/Stock Wall Panels | 1 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L15-5308 | L15 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| 16D5308 | Deliver/Stock Wall Panels | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L16-5308 | L16- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| 17D5308 | Deliver/Stock Wall Panels | 1 | 0 | 14-May-14 A | 14-May-14 A | |
| L17-5308 | L17 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 20-May-14 A | 11-Jun-14 A | |
| LL2-5308 | LL2 Thru L4 - Support Frame/Sheathing for Metal Wa | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL1-5308 | LL1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| L1-5308 | L1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| **Level 1** | | | | | | |
| L3-5102 | L3- Storefront Frames | 7 | 0 | 18-Aug-14 A | 29-Sep-14 A | |
| L1-5102 | L1 - Storefront Frames (excl. Main Entry Facade) | 8 | 0 | 02-Sep-14 A | 11-Sep-14 A | |
| L1-5104 | L1 - Storefront Glazing (excl. Main Entry Facade) | 4 | 0 | 19-Sep-14 A | 24-Sep-14 A | |
| EP-5110 | L1 - Revolving Doors | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L3-5104 | L3 - Storefront Glazing | 3 | 0 | 30-Sep-14 A | 03-Oct-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Levels 3-4** | | | | | | |
| L3-5130 | L3 - Install Punch Windows | 5 | 0 | 24-Feb-14 A | 10-Mar-14 A | |
| L4-5130 | L4 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 12-Mar-14 A | |
| L5-5130 | L5 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L6-5130 | L6- Install Punch Windows | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L7-5130 | L7 - Install Punch Windows | 5 | 0 | 18-Mar-14 A | 21-Mar-14 A | |
| L8-5130 | L8 - Install Punch Windows | 5 | 0 | 24-Mar-14 A | 28-Mar-14 A | |
| L9-5130 | L9 - Install Punch Windows | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L10-5130 | L10 - Install Punch Windows | 5 | 0 | 08-Apr-14 A | 11-Apr-14 A | |

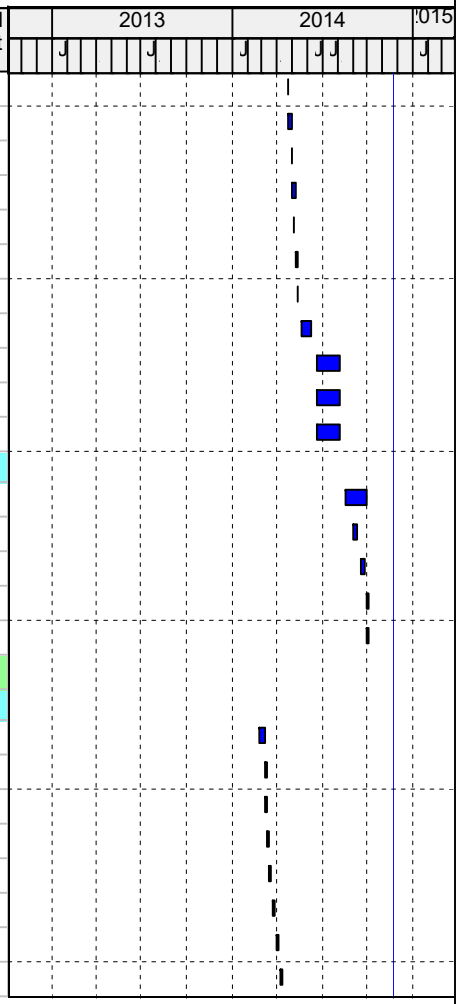


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-5130 | L11 - Install Punch Windows | 5 | 0 | 14-Apr-14 A | 21-Apr-14 A | |
| L12-5130 | L12 - Install Punch Windows | 5 | 0 | 22-Apr-14 A | 25-Apr-14 A | |
| L14-5130 | L14 - Install Punch Windows | 5 | 0 | 28-Apr-14 A | 05-May-14 A | |
| L15-5130 | L15 - Install Punch Windows | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| L16-5130 | L16 - Install Punch Windows | 5 | 0 | 12-May-14 A | 20-May-14 A | |
| L17-5130 | L17 - Install Punch Windows | 5 | 0 | 27-May-14 A | 16-Jun-14 A | |
| Roofs | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| RF-4026 | L1 - City Park - Protection Board | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| **Pool Membrane - (elev 18')** | | | | | | |
| RF-4034 | Pool - Install plumbing | 3 | 0 | 20-Oct-14 A | 22-Oct-14 A | |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |
| RF-4010 | AR - Set Mechanical Equipment | 5 | 0 | 10-Jun-14 A | 12-Jun-14 A | |
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 10 | 0 | 04-Aug-14 A | 27-Aug-14 A | |
| RF-4012 | L2.5 Horseshoe - Install corrugated metal panels | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 8 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |
| PC-4008 | RF - Entry / Porte Cochere Roofing System | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | RF - Upper Ballroom Roofing System | 3 | 0 | 28-Jul-14 A | 31-Jul-14 A | |
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 4 | 0 | 31-Jul-14 A | 04-Aug-14 A | |
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |
| RF-4018 | TR - Terrace Roof - Green Roofing System | 5 | 0 | 10-Sep-14 A | 19-Sep-14 A | |

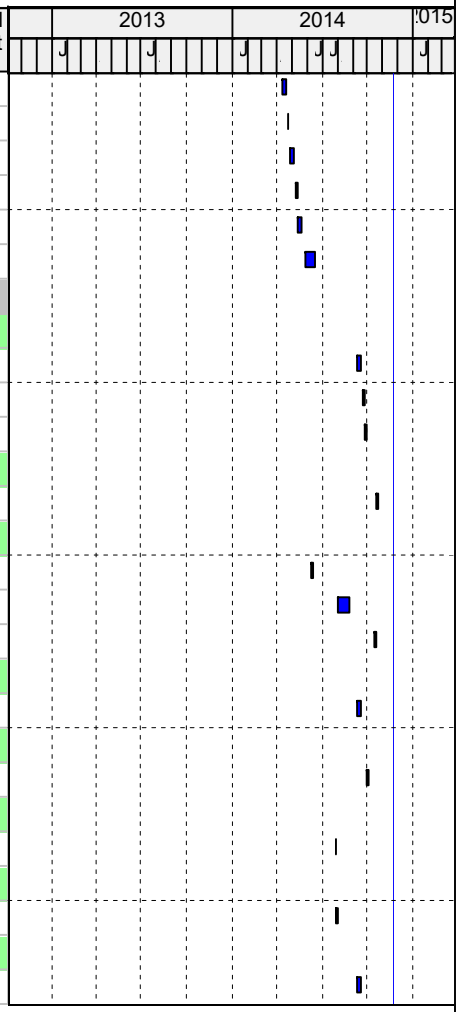



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| RF-4020 | TR - Terrace Roof - Install sheet metal capping | 1 | 1 | 03-Dec-14 | 03-Dec-14 | 52 |
| RF-4022 | TR - Terrace Roof - Install deocrative metal railing | 3 | 3 | 04-Dec-14 | 10-Dec-14 | 52 |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Perimeter Framing / Sul | 10 | 0 | 02-Jun-14 A | 08-Jul-14 A | |
| RF-4002 | Tower Roof - Roofing System | 10 | 0 | 20-Aug-14 A | 17-Sep-14 A | |
| **PH - Roof - (elev 173')** | | | | | | |
| RF-4030 | PH - Roofing System | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| RF-4032 | PH - Coping / Flashing [DELETED] | 3 | 0 | 01-Sep-14 A | 01-Sep-14 A | |
| **Rough-In's** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6002 | LL4 - Layout | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| LL4-6008 | LL4 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL4-6012 | LL4 - Fire Sprinkler Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6014 | LL4 - Plumbing Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6018 | LL4 - HVAC Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6004 | LL4 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL4-6016 | LL4 - Electrical Rl | 10 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties Rl | 8 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6010 | LL4 - Elevator pits | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| LL4-6020 | LL4 - H Mtl Frames | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL4-6024 | LL4 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6002 | LL3 - Layout | 1 | 0 | 19-Nov-13 A | 19-Nov-13 A | |
| LL3-6008 | LL3 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL3-6012 | LL3 - Fire Sprinkler Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |

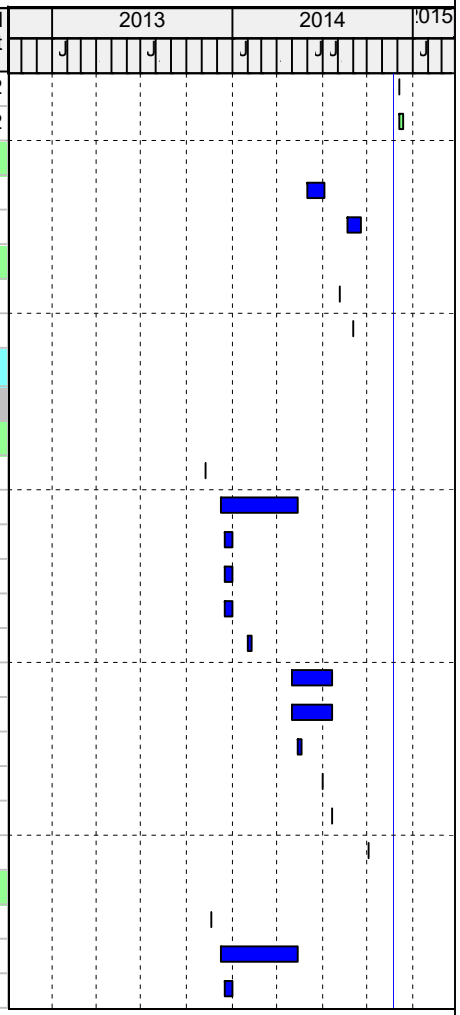



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-6014 | LL3 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6018 | LL3 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6004 | LL3 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL3-6020 | LL3 - H Mtl Frames | 3 | 0 | 08-May-14 A | 09-May-14 A | |
| LL3-6010 | LL3 - F/P Curbs | 5 | 0 | 19-May-14 A | 19-May-14 A | |
| LL3-6016 | LL3 - Electrical RI | 2 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties RI | 8 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL3-6024 | LL3 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6002 | LL2 - Layout | 1 | 0 | 14-Jan-14 A | 14-Jan-14 A | |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| LL2-6012 | LL2 - Fire Sprinkler RI | 10 | 0 | 21-Jan-14 A | 03-Feb-14 A | |
| LL2-6014 | LL2 - Plumbing RI | 10 | 0 | 21-Jan-14 A | 14-Feb-14 A | |
| LL2E-6016 | LL2 - Electrical RI | 8 | 0 | 03-Feb-14 A | 17-Mar-14 A | |
| LL2-6016 | LL2 - Electrical RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2-6018 | LL2 - HVAC RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2–6004 | LL2 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL2E-6004 | LL2 - CMU Walls | 10 | 0 | 04-Mar-14 A | 09-May-14 A | |
| LL2E-6012 | LL2 - Fire Sprinkler RI | 8 | 0 | 21-Mar-14 A | 01-Apr-14 A | |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 24-Apr-14 A | |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 3 | 0 | 23-Apr-14 A | 21-Jul-14 A | |
| LL2E-6020 | LL2 - H Mtl Frames | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| LL2-6020 | LL2 - H Mtl Frames | 3 | 0 | 12-May-14 A | 13-May-14 A | |
| LL2E-6008 | LL2 - Int Wall Framing | 5 | 0 | 13-May-14 A | 22-Jun-14 A | |
| LL2E-6014 | LL2 - Plumbing RI | 8 | 0 | 13-May-14 A | 30-May-14 A | |
| LL2E-6018 | LL2 - HVAC RI | 8 | 0 | 13-May-14 A | 04-Aug-14 A | |

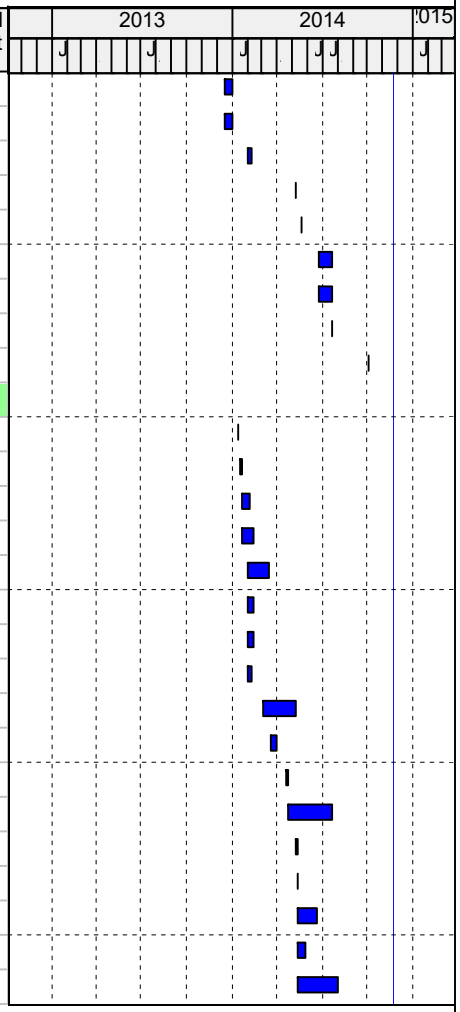


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2E-6022 | LL2 - Fire Alarm / Elec Specialties RI (East of 10) | 8 | 0 | 13-May-14 A | 22-Sep-14 A | |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties RI (West of 10) | 8 | 0 | 19-May-14 A | 22-Sep-14 A | |
| LL2-6015 | LL2 - Main Elect Room Set Equip / RI - Power to Ma | 15 | 0 | 30-Jun-14 A | 26-Sep-14 A | |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 0 | 16-Jul-14 A | 21-Jul-14 A | |
| LL2-6024 | LL2 - Inspections | 2 | 0 | 15-Sep-14 A | 03-Oct-14 A | |
| LL2-6010 | LL2 - F/P Curbs @ Parking | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 53 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6002 | Layout | 3 | 0 | 03-Jan-14 A | 08-Jan-14 A | |
| LL1-6008 | Int Wall Framing & Inspection | 6 | 0 | 08-Jan-14 A | 21-Jul-14 A | |
| LL1-Z2-6002 | Layout | 3 | 0 | 08-Jan-14 A | 14-Jan-14 A | |
| LL1-Z3-6002 | Layout | 3 | 0 | 14-Jan-14 A | 17-Jan-14 A | |
| LL1-Z2-6008 | Int Wall Framing & Inspection | 6 | 0 | 17-Jan-14 A | 01-Aug-14 A | |
| LL1-Z3-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-Jan-14 A | 04-Aug-14 A | |
| LL1-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 09-May-14 A | |
| LL1-Z2-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 28-Apr-14 A | |
| LL1-Z3-6004 | CMU Walls (At All Areas North of Q-Line) | 3 | 0 | 03-Feb-14 A | 13-May-14 A | |
| LL1C-6012 | Complete Fire Sprinkler RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6016 | Complete Electrical RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 10 | 0 | 17-Feb-14 A | 16-Sep-14 A | |
| LL1C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 30-Apr-14 A | |
| LL1-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-Z2-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |

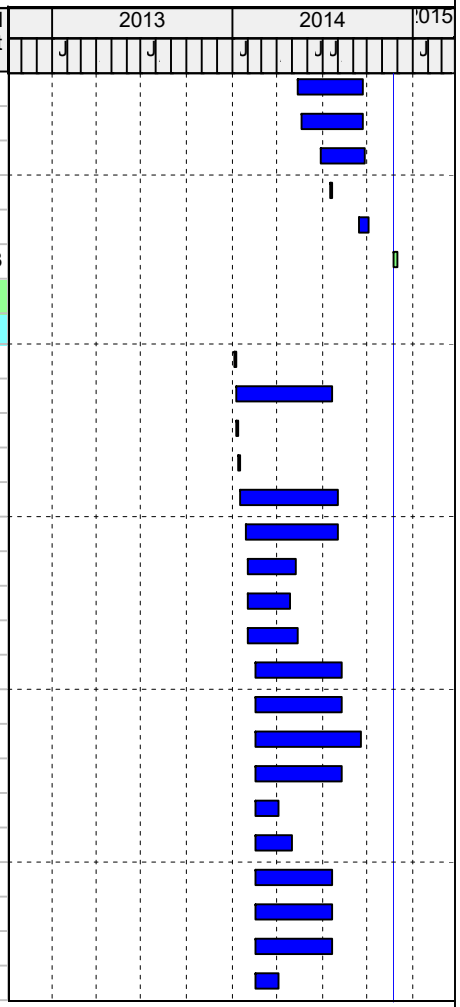


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z3-6012 | Fire Sprinkler RI (At All Areas North of Q-Line) | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z3-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 11-Sep-14 A | |
| LL1-Z3-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z2C-6012 | Complete Fire Sprinkler RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6014 | Complete Plumbing RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6016 | Complete Electrical RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 15 | 0 | 24-Feb-14 A | 15-Sep-14 A | |
| LL1-Z2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2-6020 | Hollow Metal Door Frames | 5 | 0 | 17-Mar-14 A | 04-Apr-14 A | |
| LL1-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| LL1-Z3-6020 | Hollow Metal Door Frames (At All Areas North of Q-Lir | 1 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| L1B-6004 | CMU Walls [including East Service Corridor] | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L1L-6002 | Layout [including back of house] | 3 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 29-Apr-14 A | |
| L1B-6008 | Int Wall Framing & Inspection | 6 | 0 | 21-Apr-14 A | 08-Aug-14 A | |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 5 | 0 | 25-Apr-14 A | 21-Jul-14 A | |
| LL1C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L1K-6004 | CMU Walls [including public restroom] | 3 | 0 | 05-May-14 A | 08-May-14 A | |
| L1K-6002 | Layout [including public restroom] | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| L1K-6008 | Int Wall Framing & Inspection | 4 | 0 | 09-May-14 A | 22-Aug-14 A | |
| L1B-6002 | Layout [including East Service Corridor] | 3 | 0 | 14-May-14 A | 27-May-14 A | |

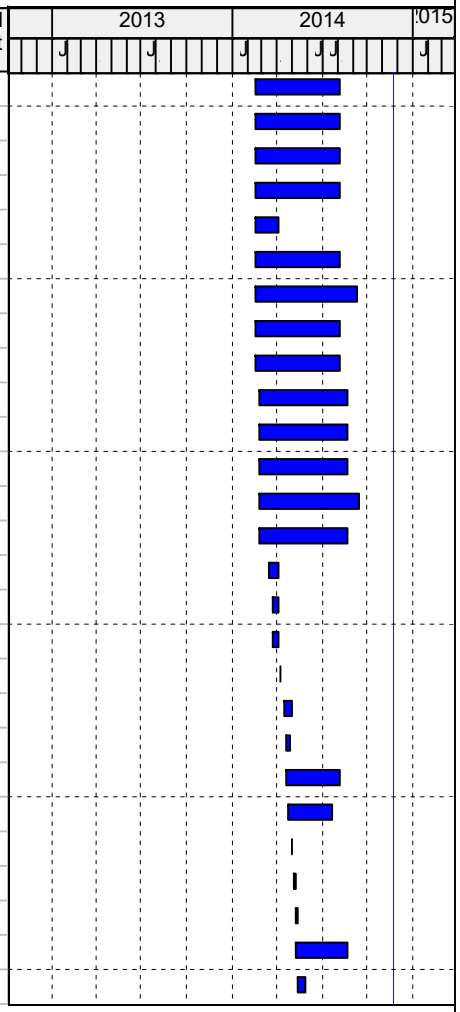



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-May-14 A | 06-Oct-14 A | |
| L1L-6004 | CMU Walls [including back of house] | 3 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L1K-6012 | Fire Sprinkler RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6014 | Plumbing RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6016 | Electrical RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1K-6018 | HVAC RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1B-6014 | Plumbing RI [including East Service Corridor] | 10 | 0 | 16-Jun-14 A | 24-Jun-14 A | |
| L1B-6018 | HVAC RI | 10 | 0 | 20-Jun-14 A | 15-Aug-14 A | |
| L1B-6012 | Fire Sprinkler RI | 10 | 0 | 21-Jun-14 A | 15-Aug-14 A | |
| L1L-6018 | HVAC RI | 5 | 0 | 23-Jun-14 A | 13-Oct-14 A | |
| L1L-6014 | Plumbing RI | 5 | 0 | 24-Jun-14 A | 28-Oct-14 A | |
| L1L-6010 | CMU Seismic Clips [including back of house] [DELET | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1L-6012 | Fire Sprinkler RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |
| L1L-6016 | Electrical RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |
| L1L-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 27-Jun-14 A | 13-Oct-14 A | |
| L1K-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 27-Jun-14 A | 29-Sep-14 A | |
| LL1-Z3-6009 | Frame Ceilings [DELETED] | 4 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1B-6016 | Electrical RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| L1B-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| LL1-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-Z2-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L1B-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-6024 | Inspections for Cover | 1 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L1B-6020 | Hollow Metal Door Frames | 5 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| LL1-Z3-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L1K-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 06-Aug-14 A | |
| LL1-Z2-6024 | Inspections for Cover | 2 | 0 | 07-Aug-14 A | 08-Aug-14 A | |

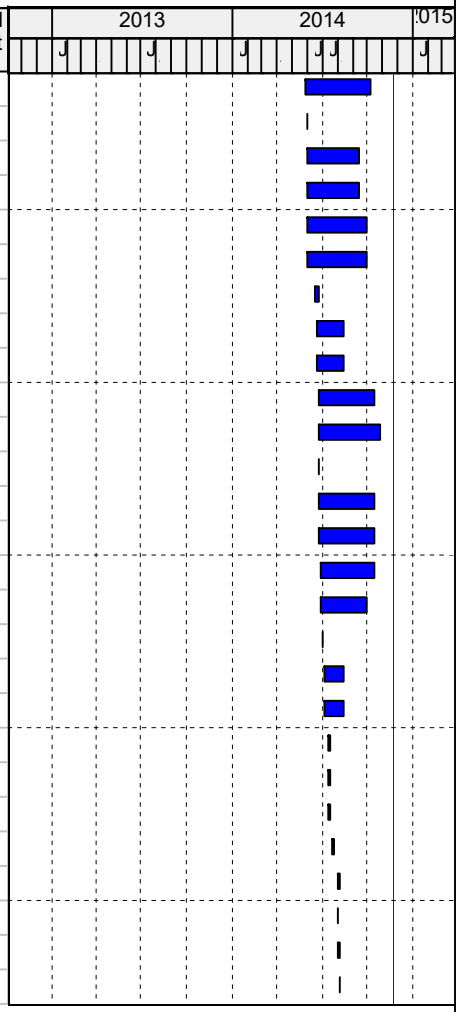



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-6020 | Hollow Metal Door Frames | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-Z2-6009 | Frame Ceilings & Inspection | 6 | 0 | 22-Aug-14 A | 13-Oct-14 A | |
| L1L-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Aug-14 A | 13-Oct-14 A | |
| LL1-6009 | Frame Ceilings & Inspection (except for bar redesign | 9 | 0 | 02-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3-6024 | Inspections for Cover | 2 | 0 | 12-Sep-14 A | 12-Sep-14 A | |
| LL1-Z3C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6016 | Complete Electrical RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3C-6018 | Complete HVAC RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| L1KC-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 4 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L1B-6024 | Inspections for Cover (Main Ballroom N/S/W Walls & | 3 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1K-6024 | Inspections for Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1KC-6014 | Complete Plumbing RI @ Ceilings & Inspection | 4 | 0 | 02-Oct-14 A | 07-Oct-14 A | |
| L1BC-6014 | Complete Plumbing RI @ Ceilings | 7 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L1BC-6018 | Complete HVAC RI @ Ceilings | 7 | 0 | 06-Oct-14 A | 07-Nov-14 A | |
| L1KC-6018 | Complete HVAC RI @ Ceilings & Inspection | 4 | 0 | 06-Oct-14 A | 10-Nov-14 A | |
| L1KC-6016 | Complete Electrical RI @ Ceilings & Inspection | 3 | 0 | 20-Oct-14 A | 10-Nov-14 A | |
| L1KC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 3 | 0 | 20-Oct-14 A | 10-Nov-14 A | |
| L1L-6024 | Inspections for Cover | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L1B-6009 | Frame Ceilings | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 15 |
| L1BC-6012 | Complete Fire Sprinkler RI @ Ceilings | 6 | 6 | 24-Nov-14 | 03-Dec-14 | 20 |
| L1L-6009 | Frame Ceilings & Inspection | 13 | 13 | 24-Nov-14 | 12-Dec-14 | 0 |
| L1LC-6012 | Complete Fire Sprinkler RI @ Ceilings | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 9 |
| L1LC-6014 | Complete Plumbing RI @ Ceilings | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 9 |
| L1LC-6016 | Complete Electrical RI @ Ceilings | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 9 |
| L1LC-6018 | Complete HVAC RI @ Ceilings | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 9 |

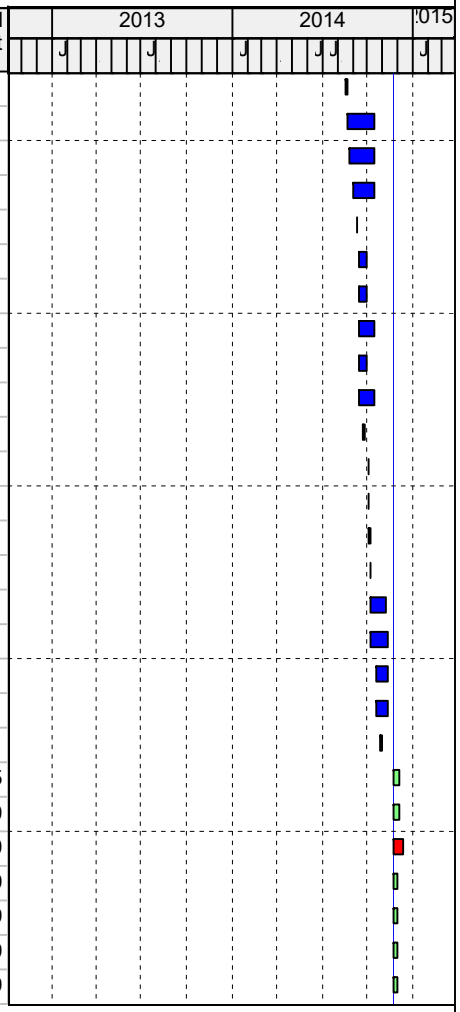



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1LC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 9 |
| L1K-6009 | Frame Ceilings [public restroom] | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 16 |
| L1BC-6016 | Complete Electrical RI @ Ceilings & Inspection | 6 | 6 | 03-Dec-14 | 10-Dec-14 | 15 |
| L1BC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 6 | 6 | 03-Dec-14 | 10-Dec-14 | 15 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 0 | 17-Apr-14 A | 09-May-14 A | |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6006 | L2 - Support Frame/Sheathing for Metal Panels | 6 | 0 | 23-Apr-14 A | 07-Aug-14 A | |
| L02-6008 | L2 - Int Wall Framing | 10 | 0 | 25-Apr-14 A | 17-Jul-14 A | |
| L02-6014 | L2 - Plumbing RI | 15 | 0 | 28-Apr-14 A | 07-Aug-14 A | |
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 0 | 28-Apr-14 A | 09-May-14 A | |
| L02-6004 | L2 - CMU Walls | 5 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L02-6002 | L2 - Layout | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L02-6018 | L2 - HVAC RI (including equipment) | 20 | 0 | 18-Jun-14 A | 10-Sep-14 A | |
| L02-6016 | L2 - Electrical RI | 10 | 0 | 24-Jun-14 A | 14-Aug-14 A | |
| L02-6022 | L2 - Fire Alarm / Elec Specialties RI | 10 | 0 | 24-Jun-14 A | 10-Oct-14 A | |
| L02-6012 | L2 - Fire Sprinkler RI | 10 | 0 | 26-Jun-14 A | 07-Aug-14 A | |
| L02-6020 | L2 - H Mtl Frames | 5 | 0 | 11-Jul-14 A | 17-Jul-14 A | |
| L02-6024 | L2 - Inspections - North Half | 2 | 0 | 10-Oct-14 A | 20-Oct-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L07-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 01-Apr-11 A | 11-Apr-11 A | |
| L04-6012 | Fire Sprinkler Mains | 5 | 0 | 01-Feb-14 A | 03-Apr-14 A | |
| L03-8219 | HVAC Risers | 5 | 0 | 11-Feb-14 A | 23-Mar-14 A | |
| L03-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 11-Feb-14 A | 03-Mar-14 A | |
| L03-6002 | Layout | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |

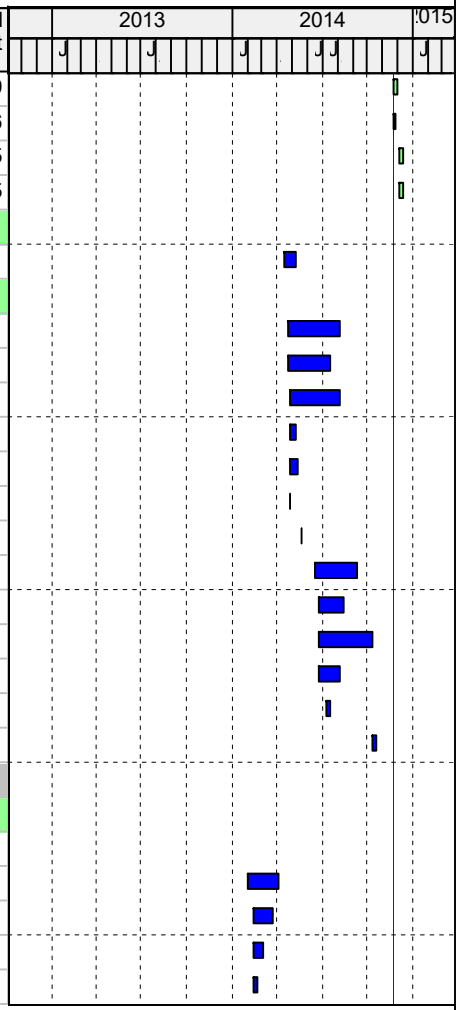



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8219 | HVAC Risers | 5 | 0 | 13-Feb-14 A | 23-Mar-14 A | |
| L05-8219 | HVAC Risers | 5 | 0 | 17-Feb-14 A | 03-Mar-14 A | |
| L03-6008 | Frame Shaft Walls | 3 | 0 | 18-Feb-14 A | 26-Mar-14 A | |
| L04-6002 | Layout | 5 | 0 | 19-Feb-14 A | 25-Feb-14 A | |
| L04-6008 | Frame Shaft Walls | 3 | 0 | 20-Feb-14 A | 26-Mar-14 A | |
| L03-6011 | PreRock Shafts | 2 | 0 | 24-Feb-14 A | 25-Mar-14 A | |
| L03-6010 | Frame Walls | 5 | 0 | 25-Feb-14 A | 25-Mar-14 A | |
| L05-6002 | Layout | 5 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| L04-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 28-Feb-14 A | 05-Mar-14 A | |
| L03-6016 | Electrical RI | 5 | 0 | 03-Mar-14 A | 04-Apr-14 A | |
| L03-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 12-Mar-14 A | |
| L04-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 13-Mar-14 A | |
| L04-6010 | Frame Walls | 5 | 0 | 04-Mar-14 A | 05-Jun-14 A | |
| L05-6008 | Frame Shaft Walls | 3 | 0 | 05-Mar-14 A | 27-Mar-14 A | |
| L06-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L07-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L05-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 06-Mar-14 A | 21-Mar-14 A | |
| L03-6020 | Install Hollow Metal Frames | 3 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L04-6020 | Install Hollow Metal Frames | 3 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L05-6010 | Frame Walls | 5 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L06-6002 | Layout | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L04-6011 | PreRock Shafts | 2 | 0 | 18-Mar-14 A | 25-Mar-14 A | |
| L05-6009 | Inspect Shafts | 1 | 0 | 18-Mar-14 A | 18-Mar-14 A | |
| L05-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| L06-6008 | Frame Shaft Walls | 3 | 0 | 19-Mar-14 A | 03-Apr-14 A | |
| L06-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 27-Mar-14 A | |
| L04-6016 | Electrical RI | 5 | 0 | 20-Mar-14 A | 09-Apr-14 A | |

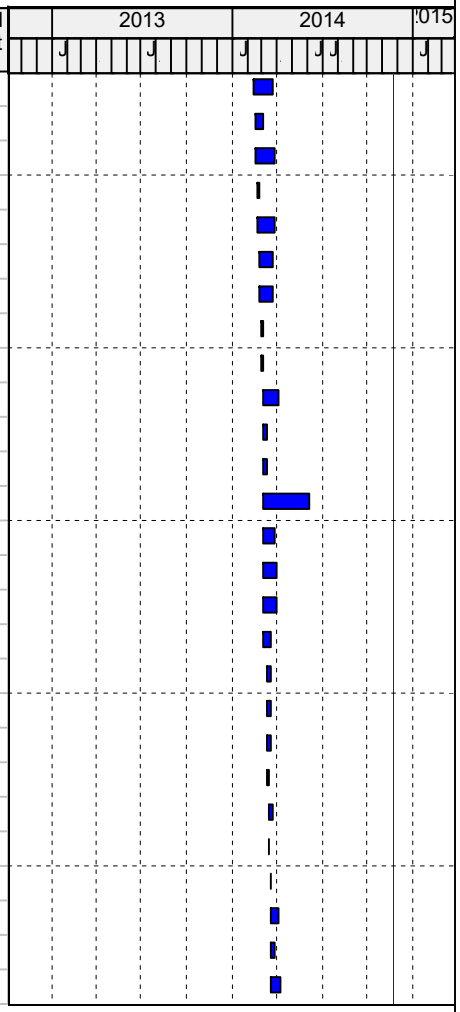



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 26-Mar-14 A | |
| L06-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 07-Apr-14 A | |
| L07-6002 | Layout | 5 | 0 | 24-Mar-14 A | 30-Apr-14 A | |
| L03-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L03-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L05-6016 | Electrical RI | 5 | 0 | 25-Mar-14 A | 05-Jun-14 A | |
| L04-6019 | Complete Top Out GWB | 2 | 0 | 26-Mar-14 A | 06-Jun-14 A | |
| L05-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L06-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| L03-6019 | Complete Top Out GWB | 2 | 0 | 27-Mar-14 A | 02-May-14 A | |
| L08-6002 | Layout | 5 | 0 | 27-Mar-14 A | 02-Apr-14 A | |
| L05-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 28-Mar-14 A | 03-Apr-14 A | |
| L06-6010 | Frame Walls | 5 | 0 | 28-Mar-14 A | 07-Apr-14 A | |
| L03-6012 | Fire Sprinkler Mains | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L07-6008 | Frame Shaft Walls | 3 | 0 | 31-Mar-14 A | 03-Apr-14 A | |
| L05-6019 | Complete Top Out GWB | 2 | 0 | 01-Apr-14 A | 08-Apr-14 A | |
| L08-6008 | Frame Shaft Walls | 3 | 0 | 02-Apr-14 A | 21-Apr-14 A | |
| L03-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L04-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L05-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L06-6016 | Electrical RI | 5 | 0 | 03-Apr-14 A | 15-Apr-14 A | |
| L07-6009 | Inspect Shafts | 1 | 0 | 03-Apr-14 A | 03-Apr-14 A | |
| L07-6011 | PreRock Shafts | 2 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| L05-6012 | Fire Sprinkler Mains | 5 | 0 | 04-Apr-14 A | 30-Apr-14 A | |
| L06-6012 | Fire Sprinkler Mains | 5 | 0 | 07-Apr-14 A | 30-Apr-14 A | |

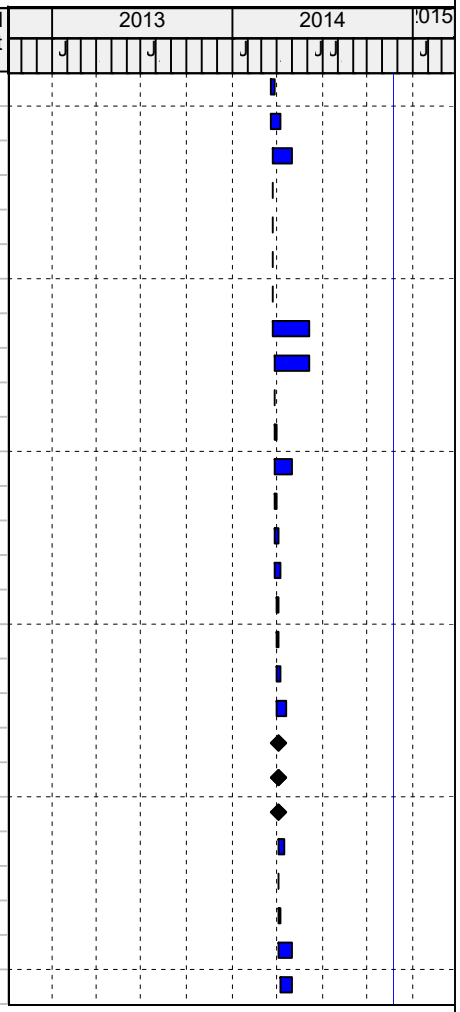



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L06-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L07-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| L07-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L03-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L03-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L04-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L06-6009 | Inspect Shafts | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L06-6019 | Complete Top Out GWB | 2 | 0 | 08-Apr-14 A | 18-Apr-14 A | |
| L07-6010 | Frame Walls | 5 | 0 | 08-Apr-14 A | 15-Apr-14 A | |
| L08-6011 | PreRock Shafts | 2 | 0 | 08-Apr-14 A | 23-Apr-14 A | |
| L09-6002 | Layout | 5 | 0 | 08-Apr-14 A | 26-Apr-14 A | |
| L03-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 09-Apr-14 A | 08-May-14 A | |
| L03-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L05-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 09-Apr-14 A | 14-Apr-14 A | |
| L08-6009 | Inspect Shafts | 1 | 0 | 09-Apr-14 A | 25-Apr-14 A | |
| L09-6008 | Frame Shaft Walls | 3 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| L08-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| L04-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 15-Apr-14 A | 16-Apr-14 A | |
| L07-6012 | Fire Sprinkler Mains | 5 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| L07-6016 | Electrical RI | 5 | 0 | 15-Apr-14 A | 12-May-14 A | |
| L07-6020 | Install Hollow Metal Frames | 3 | 0 | 16-Apr-14 A | 23-Apr-14 A | |
| L05-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 17-Apr-14 A | 25-Apr-14 A | |
| L06-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 17-Apr-14 A | 12-May-14 A | |
| L06-6023 | Inspection of Exterior Framing | 0 | 0 | 17-Apr-14 A | | |
| L09-8219 | HVAC Risers | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L09-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |

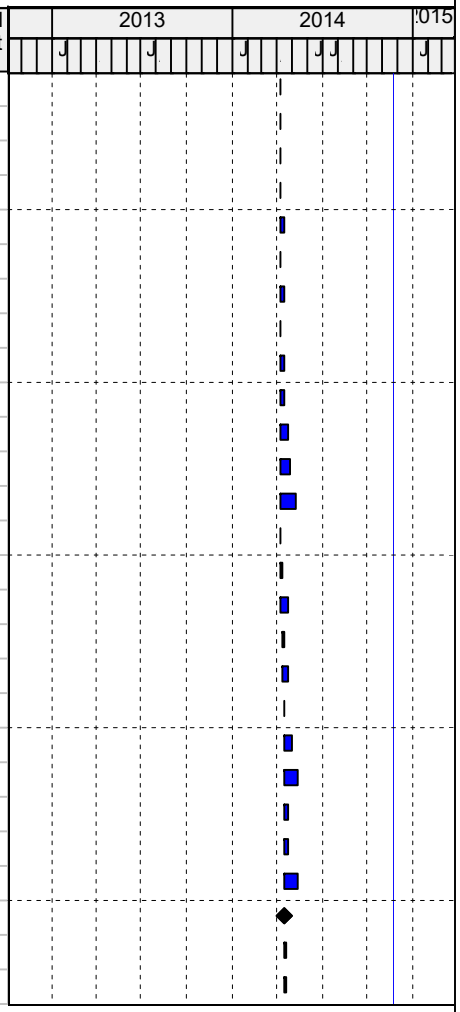



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 18-Apr-14 A | 20-Apr-14 A | |
| L04-6028 | PreRock at Heat Pumps | 2 | 0 | 20-Apr-14 A | 22-Apr-14 A | |
| L08-8219 | HVAC Risers | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6009 | Inspect Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6011 | PreRock Shafts | 2 | 0 | 22-Apr-14 A | 24-Apr-14 A | |
| L04-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L06-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 23-Apr-14 A | 25-Apr-14 A | |
| L08-6020 | Install Hollow Metal Frames | 3 | 0 | 23-Apr-14 A | 13-May-14 A | |
| L11-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L11-8220 | Plumbing Risers - Install | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L04-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L09-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L10-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L10-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 20-May-14 A | |
| L12-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L04-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 25-Apr-14 A | 11-Jun-14 A | |
| L04-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L09-6010 | Frame Walls | 5 | 0 | 25-Apr-14 A | 20-May-14 A | |
| L09-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L10-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L11-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 30-Apr-14 A | |
| L12-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L08-6010 | Frame Walls | 5 | 0 | 26-Apr-14 A | 30-Apr-14 A | |
| L10-6002 | Layout | 5 | 0 | 27-Apr-14 A | 27-Apr-14 A | |
| L04-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 28-Apr-14 A | 30-Apr-14 A | |

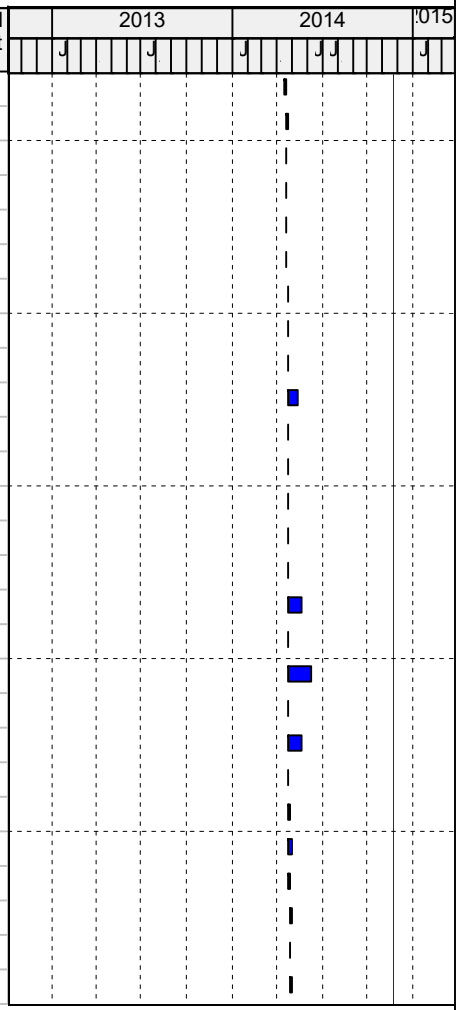



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6018 | HVAC RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6028 | PreRock at Heat Pumps | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L07-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 28-Apr-14 A | 12-May-14 A | |
| L10-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-Apr-14 A | 22-May-14 A | |
| L11-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L12-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L05-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| L05-6028 | PreRock at Heat Pumps | 2 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L06-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 09-May-14 A | |
| L06-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L06-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L08-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L08-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L09-6020 | Install Hollow Metal Frames | 3 | 0 | 29-Apr-14 A | 20-May-14 A | |
| L09-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L10-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L04-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 30-Apr-14 A | 02-May-14 A | |
| L09-6019 | Complete Top Out GWB | 2 | 0 | 30-Apr-14 A | 06-Jun-14 A | |
| L11-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |

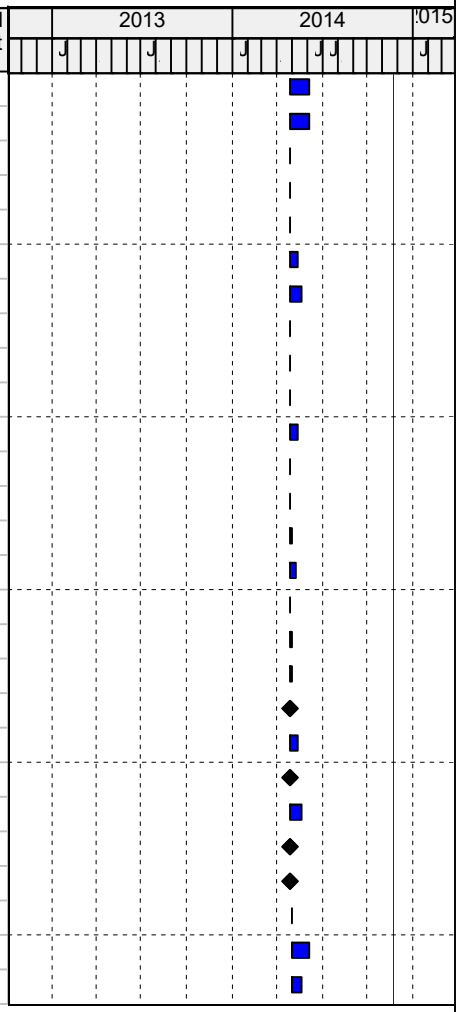



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L03-6028 | PreRock at Heat Pumps | 2 | 0 | 01-May-14 A | 02-May-14 A | |
| L05-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L06-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L03-6014 | Set Tubs & Plumbing RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L05-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L05-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| L06-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L06-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 09-May-14 A | |
| L03-6018 | HVAC RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L03-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 06-May-14 A | 06-May-14 A | |
| L07-6014 | Set Tubs & Plumbing RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L07-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 06-May-14 A | 09-May-14 A | |
| L03-6004 | CMU Wall/Clips | 3 | 0 | 07-May-14 A | 08-May-14 A | |
| L03-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L03-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 08-May-14 A | 13-May-14 A | |
| L03-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6004 | CMU Walls | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6018 | HVAC RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L11-6010 | Frame Walls | 5 | 0 | 09-May-14 A | 15-May-14 A | |
| L05-6014 | Set Tubs & Plumbing RI | 5 | 0 | 12-May-14 A | 05-Jun-14 A | |
| L07-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 0 | 12-May-14 A | 13-May-14 A | |

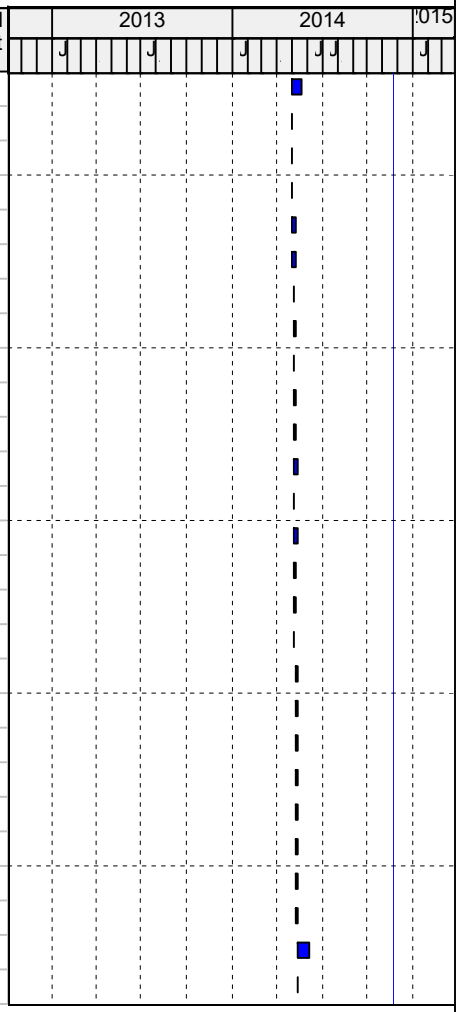


Actual Work | Remaining Work | Critical Remai... | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6020 | Install Hollow Metal Frames | 3 | 0 | 12-May-14 A | 14-May-14 A | |
| L11-6019 | Complete Top Out GWB | 2 | 0 | 12-May-14 A | 14-May-14 A | |
| L14-6002 | Layout | 5 | 0 | 12-May-14 A | 14-May-14 A | |
| L15-6002 | Layout | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L05-6004 | CMU Walls | 3 | 0 | 13-May-14 A | 13-May-14 A | |
| L06-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 25-Jun-14 A | |
| L06-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 13-May-14 A | 14-Jul-14 A | |
| L07-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 05-Jun-14 A | |
| L07-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| L07-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 13-May-14 A | 13-May-14 A | |
| L14-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L16-6002 | Layout | 5 | 0 | 13-May-14 A | 16-May-14 A | |
| L06-6004 | CMU Walls | 3 | 0 | 14-May-14 A | 14-May-14 A | |
| L07-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 15-May-14 A | |
| L08-6012 | Fire Sprinkler Mains | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6002 | Layout | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L07-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6014 | Set Tubs & Plumbing RI | 5 | 0 | 16-May-14 A | 25-Jun-14 A | |
| L08-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L11-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L12-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L07-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L08-6028 | PreRock at Heat Pumps | 2 | 0 | 19-May-14 A | 20-May-14 A | |

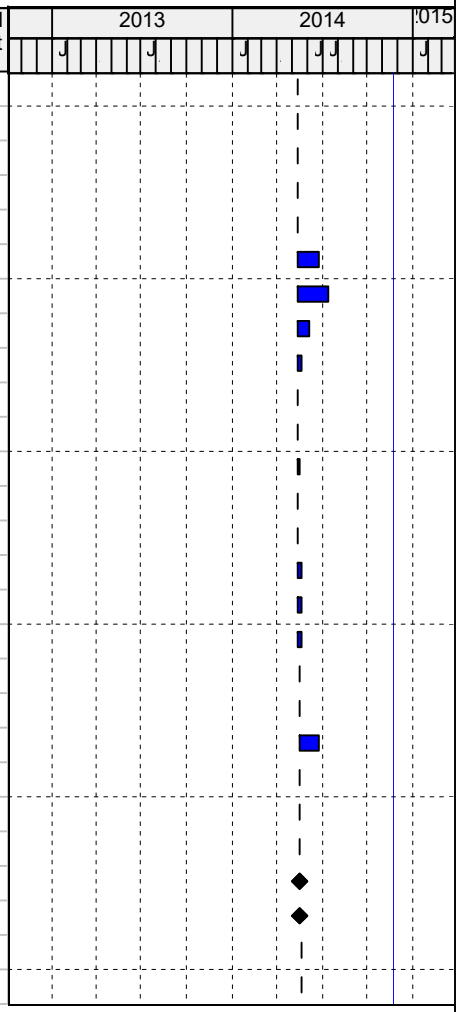


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L10-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L11-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L15-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 19-May-14 A | 19-May-14 A | |
| L07-6028 | PreRock at Heat Pumps | 2 | 0 | 20-May-14 A | 21-May-14 A | |
| L07-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L08-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 20-May-14 A | 21-May-14 A | |
| L10-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L11-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L14-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L07-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 21-May-14 A | 27-May-14 A | |
| L08-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L08-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L09-6028 | PreRock at Heat Pumps | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L10-6014 | Set Tubs & Plumbing RI | 5 | 0 | 21-May-14 A | 27-Jun-14 A | |
| L10-6010 | Frame Walls | 5 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6019 | Complete Top Out GWB | 2 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L11-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L12-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L14-8220 | Plumbing Risers - Install | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L15-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L16-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L07-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| L08-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 22-May-14 A | 22-May-14 A | |

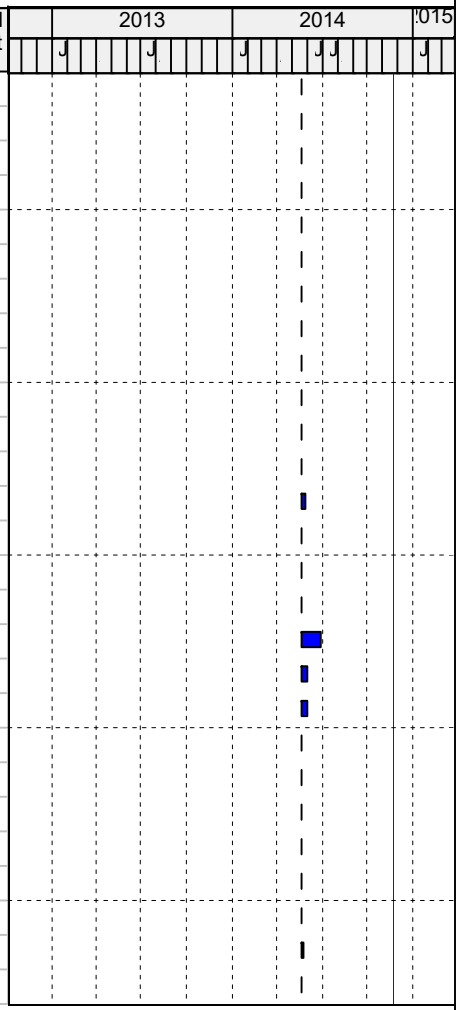



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-6012 | Fire Sprinkler Mains | 5 | 0 | 22-May-14 A | 27-May-14 A | |
| L08-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L09-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6020 | Install Hollow Metal Frames | 3 | 0 | 23-May-14 A | 03-Jun-14 A | |
| L10-6028 | PreRock at Heat Pumps | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L14-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L15-8220 | Plumbing Risers - Install | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L09-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 27-May-14 A | 27-May-14 A | |
| L12-6010 | Frame Walls | 5 | 0 | 27-May-14 A | 02-Jun-14 A | |
| L08-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L09-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 28-May-14 A | 28-May-14 A | |
| L10-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 28-May-14 A | 03-Jun-14 A | |
| L14-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L15-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-May-14 A | 30-May-14 A | |
| L16-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 28-May-14 A | 28-May-14 A | |
| L16-8220 | Plumbing Risers - Install | 2 | 0 | 28-May-14 A | 29-May-14 A | |
| L08-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 29-May-14 A | 30-May-14 A | |
| L10-6016 | Electrical RI | 5 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L10-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| L12-6012 | Fire Sprinkler Mains | 5 | 0 | 30-May-14 A | 26-Jun-14 A | |
| L12-6020 | Install Hollow Metal Frames | 3 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L15-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L17-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L17-8220 | Plumbing Risers - Install | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L10-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 02-Jun-14 A | 03-Jun-14 A | |

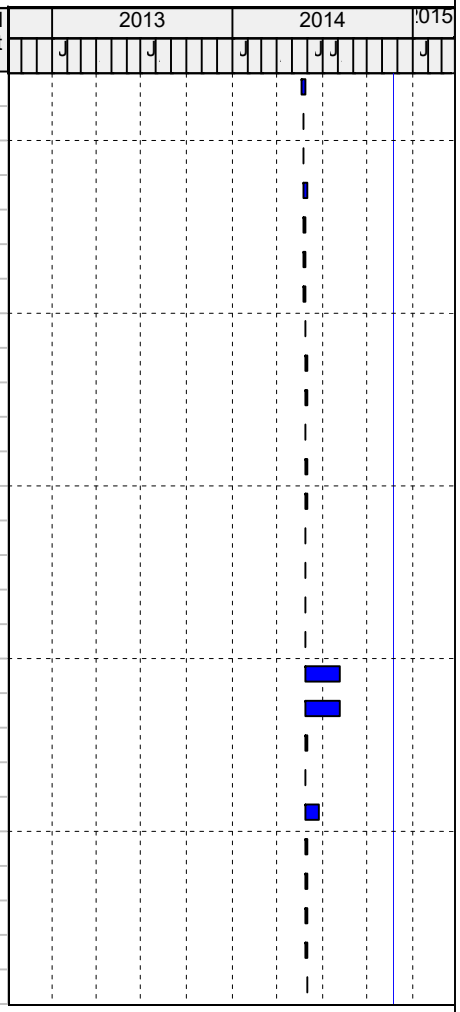



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6016 | Electrical RI | 5 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L11-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L12-6019 | Complete Top Out GWB | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L14-6020 | Install Hollow Metal Frames | 3 | 0 | 02-Jun-14 A | 05-Jun-14 A | |
| L14-6010 | Frame Walls | 5 | 0 | 02-Jun-14 A | 04-Jun-14 A | |
| L16-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| L14-6019 | Complete Top Out GWB | 2 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L16-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L10-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| L17-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 04-Jun-14 A | 11-Jun-14 A | |
| L08-6016 | Electrical RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L08-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L09-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L12-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L15-6010 | Frame Walls | 3 | 0 | 05-Jun-14 A | 11-Jun-14 A | |
| L09-6012 | Fire Sprinkler Mains | 5 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L09-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L11-6012 | Fire Sprinkler Mains | 4 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L12-6014 | Set Tubs & Plumbing RI | 4 | 0 | 06-Jun-14 A | 27-Jun-14 A | |
| L11-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jun-14 A | 11-Jun-14 A | |
| L09-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-Jun-14 A | 25-Jun-14 A | |
| L14-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L15-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L16-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L09-6016 | Electrical RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |

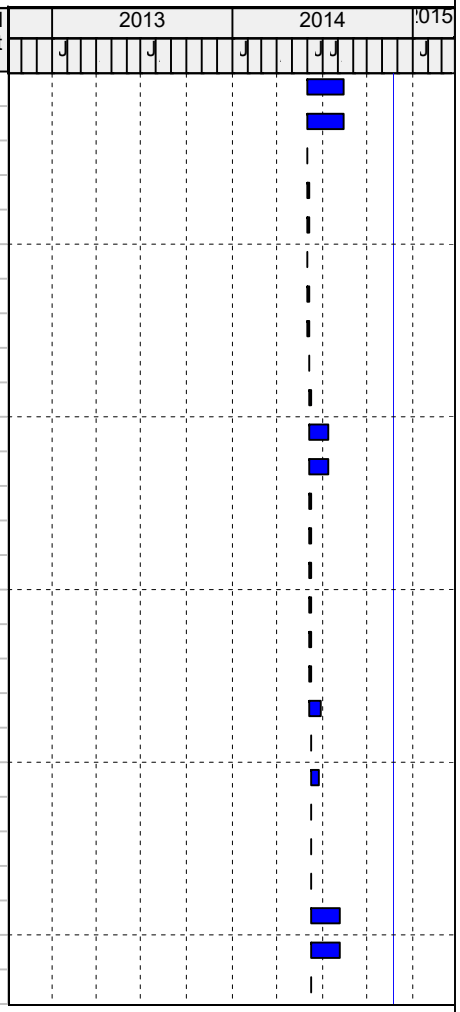



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L14-6014 | Set Tubs & Plumbing RI | 4 | 0 | 10-Jun-14 A | 21-Jul-14 A | |
| L15-6020 | Install Hollow Metal Frames | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L15-6019 | Complete Top Out GWB | 2 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6014 | Set Tubs & Plumbing RI | 4 | 0 | 11-Jun-14 A | 26-Jun-14 A | |
| L11-6028 | PreRock at Heat Pumps | 2 | 0 | 13-Jun-14 A | 14-Jun-14 A | |
| L11-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 14-Jun-14 A | 14-Jun-14 A | |
| L14-6012 | Fire Sprinkler Mains | 2 | 0 | 16-Jun-14 A | 27-Jun-14 A | |
| L14-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 18-Jun-14 A | 18-Jun-14 A | |
| L15-6023 | Inspection of Exterior Framing | 0 | 0 | 18-Jun-14 A | | |
| L17-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 18-Jun-14 A | 23-Jun-14 A | |
| L17-6010 | Frame Walls | 5 | 0 | 18-Jun-14 A | 29-Jul-14 A | |
| L10-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L12-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6023 | Inspection of Exterior Framing | 0 | 0 | 20-Jun-14 A | | |
| L15-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-Jun-14 A | 20-Jun-14 A | |
| L10-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-Jun-14 A | 23-Jun-14 A | |
| L15-6014 | Set Tubs & Plumbing RI | 5 | 0 | 22-Jun-14 A | 24-Jul-14 A | |
| L08-6018 | HVAC RI | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L12-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L14-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L15-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L08-6221 | Frame Unit Ceilings | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| L11-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 24-Jun-14 A | 27-Jun-14 A | |

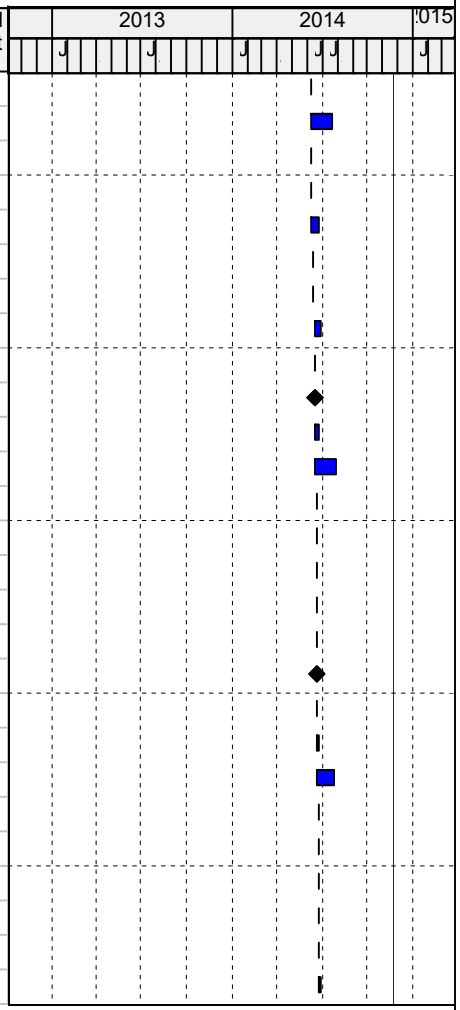



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L14-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6023 | Inspection of Exterior Framing | 0 | 0 | 24-Jun-14 A | | |
| L12-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| L12-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L14-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L15-6012 | Fire Sprinkler Mains | 2 | 0 | 25-Jun-14 A | 22-Jul-14 A | |
| L16-6023 | Inspection of Exterior Framing | 0 | 0 | 25-Jun-14 A | | |
| L03-6024 | Inspections for GWB Cover | 1 | 0 | 27-Jun-14 A | 27-Jun-14 A | |
| L09-6018 | HVAC RI | 3 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L09-6221 | Frame Unit Ceilings | 2 | 0 | 27-Jun-14 A | 30-Jun-14 A | |
| L12-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L14-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L15-6028 | PreRock at Heat Pumps | 2 | 0 | 30-Jun-14 A | 01-Jul-14 A | |
| L16-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 30-Jun-14 A | 30-Jun-14 A | |
| L16-6010 | Frame Walls | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| L16-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L15-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L15-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L04-6024 | Inspections for GWB Cover | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L10-6018 | HVAC RI | 3 | 0 | 07-Jul-14 A | 21-Jul-14 A | |
| L11-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L15-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L16-6012 | Fire Sprinkler Mains | 2 | 0 | 07-Jul-14 A | 24-Jul-14 A | |
| L16-6020 | Install Hollow Metal Frames | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L16-6028 | PreRock at Heat Pumps | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L17-6019 | Complete Top Out GWB | 1 | 0 | 07-Jul-14 A | 08-Aug-14 A | |

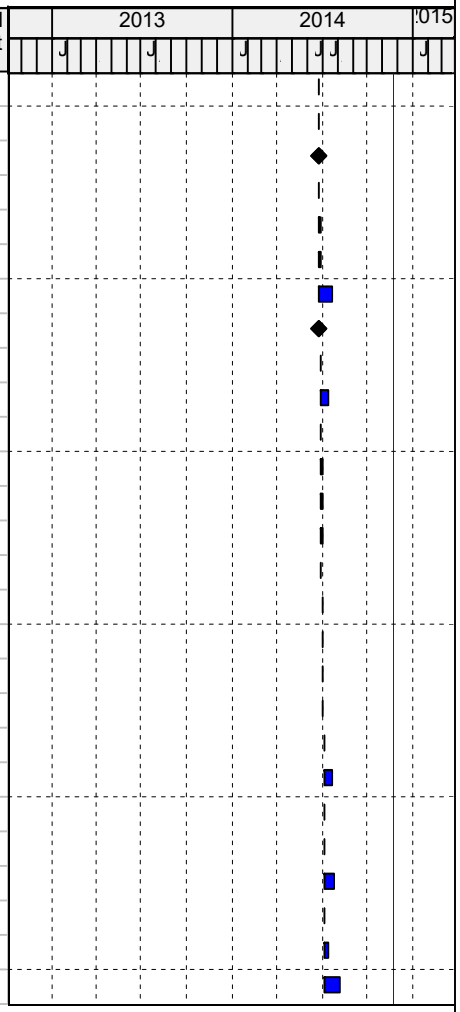



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L15-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 08-Jul-14 A | 04-Aug-14 A | |
| L17-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jul-14 A | 01-Aug-14 A | |
| L10-6221 | Frame Unit Ceilings | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| L17-6012 | Fire Sprinkler Mains | 2 | 0 | 09-Jul-14 A | 12-Aug-14 A | |
| L05-6024 | Inspections for GWB Cover | 2 | 0 | 10-Jul-14 A | 10-Jul-14 A | |
| L04-6000 | Tape/Finish GWB | 6 | 0 | 11-Jul-14 A | 23-Jul-14 A | |
| L16-6019 | Complete Top Out GWB | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L16-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L15-6018 | HVAC RI | 3 | 0 | 16-Jul-14 A | 18-Jul-14 A | |
| L16-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-6024 | Inspections for GWB Cover | 2 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6018 | HVAC RI | 3 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L16-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 21-Jul-14 A | 18-Aug-14 A | |
| L15-6013 | Fire Sprinkler Branch Lines | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| L03-6000 | Tape/Finish GWB | 6 | 0 | 23-Jul-14 A | 29-Jul-14 A | |
| L11-6018 | HVAC RI | 3 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L15-6221 | Frame Unit Ceilings | 2 | 0 | 23-Jul-14 A | 01-Aug-14 A | |
| L16-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L17-6020 | Install Hollow Metal Frames | 3 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| L11-6221 | Frame Unit Ceilings | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L12-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L14-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L14-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |

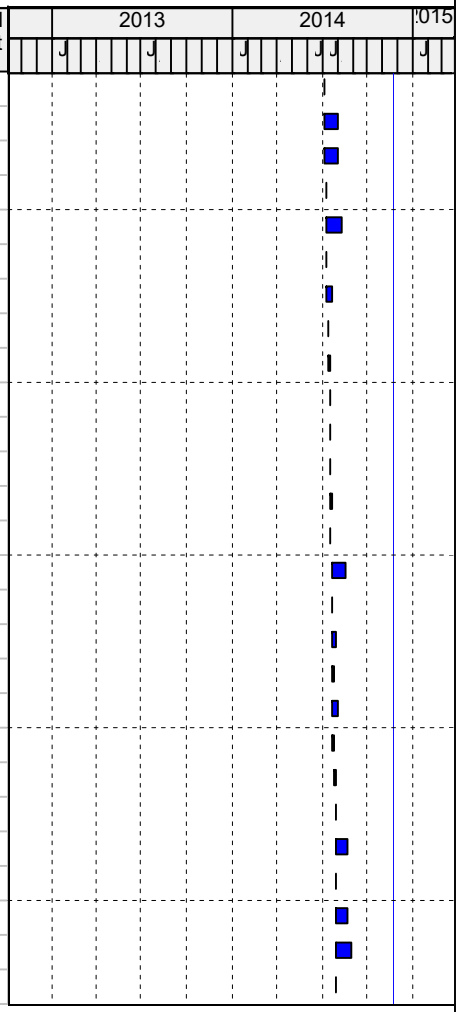



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L16-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 28-Jul-14 A | 18-Aug-14 A | |
| L07-6024 | Inspections for GWB Cover | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L12-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L05-6000 | Tape/Finish GWB | 6 | 0 | 31-Jul-14 A | 05-Aug-14 A | |
| L08-6024 | Inspections for GWB Cover | 2 | 0 | 31-Jul-14 A | 31-Jul-14 A | |
| L12-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L14-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L06-6000 | Tape/Finish GWB | 4 | 0 | 06-Aug-14 A | 11-Aug-14 A | |
| L09-6024 | Inspections for GWB Cover | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L07-6000 | Tape/Finish GWB | 5 | 0 | 07-Aug-14 A | 16-Aug-14 A | |
| L11-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 08-Aug-14 A | 14-Aug-14 A | |
| L17-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 08-Aug-14 A | 16-Sep-14 A | |
| L10-6024 | Inspections for GWB Cover | 2 | 0 | 11-Aug-14 A | 12-Aug-14 A | |
| L09-6000 | Tape/Finish GWB | 5 | 0 | 14-Aug-14 A | 19-Aug-14 A | |
| L08-6000 | Tape/Finish GWB | 5 | 0 | 16-Aug-14 A | 21-Aug-14 A | |
| L11-6024 | Inspections for GWB Cover | 2 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L16-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 18-Aug-14 A | 29-Aug-14 A | |
| L10-6000 | Tape/Finish GWB | 5 | 0 | 19-Aug-14 A | 23-Aug-14 A | |
| L16-6221 | Frame Unit Ceilings | 4 | 0 | 21-Aug-14 A | 26-Aug-14 A | |
| L17-6018 | HVAC Rl | 3 | 0 | 21-Aug-14 A | 10-Sep-14 A | |
| L12-6024 | Inspections for GWB Cover | 2 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L15-6016 | Electrical Rl | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L15-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |

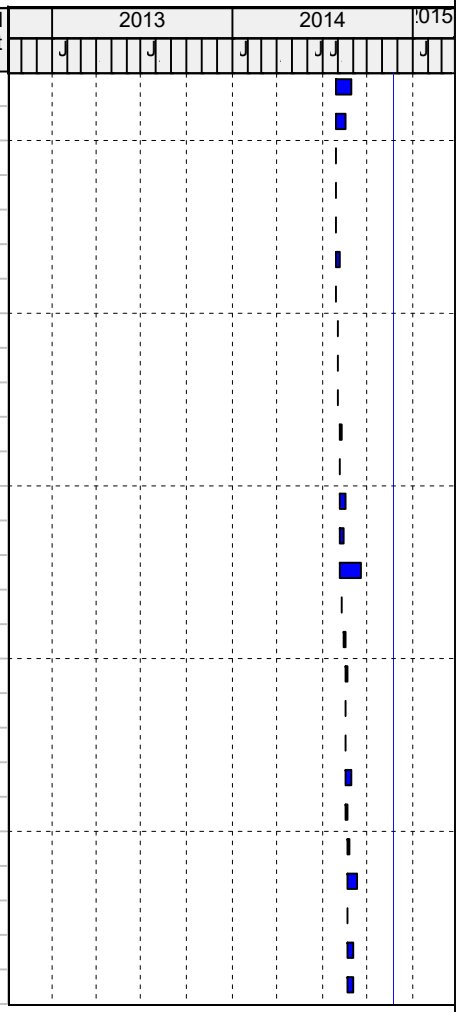



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6000 | Tape/Finish GWB | 5 | 0 | 23-Aug-14 A | 29-Aug-14 A | |
| L17-6221 | Frame Unit Ceilings | 4 | 0 | 26-Aug-14 A | 28-Aug-14 A | |
| L14-6024 | Inspections for GWB Cover | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L16-6016 | Electrical RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L16-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L12-6000 | Tape/Finish GWB | 5 | 0 | 02-Sep-14 A | 08-Sep-14 A | |
| L15-6024 | Inspections for GWB Cover | 2 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L14-6000 | Tape/Finish GWB | 5 | 0 | 06-Sep-14 A | 11-Sep-14 A | |
| L15-6000 | Tape/Finish GWB | 4 | 0 | 12-Sep-14 A | 20-Sep-14 A | |
| L17-6016 | Electrical RI | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-6028 | PreRock at Heat Pumps | 2 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L17-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L17-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L17-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 24-Sep-14 A | 27-Sep-14 A | |
| L17-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L16-6024 | Inspections for GWB Cover | 1 | 0 | 08-Oct-14 A | 09-Oct-14 A | |
| L16-6000 | Tape/Finish GWB | 4 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6024 | Inspections for GWB Cover | 1 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6000 | Tape/Finish GWB | 6 | 0 | 30-Oct-14 A | 07-Nov-14 A | |
| **Mechanical Penthouse** | | | | | | |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 0 | 11-Jun-14 A | 20-Jun-14 A | |
| PH-6006 | PH - Exterior Wall Framing (including PH roof parapet | 6 | 0 | 12-Jun-14 A | 14-Jul-14 A | |
| PH-6014 | PH - Plumbing/Piping RI | 40 | 0 | 25-Jun-14 A | 05-Nov-14 A | |

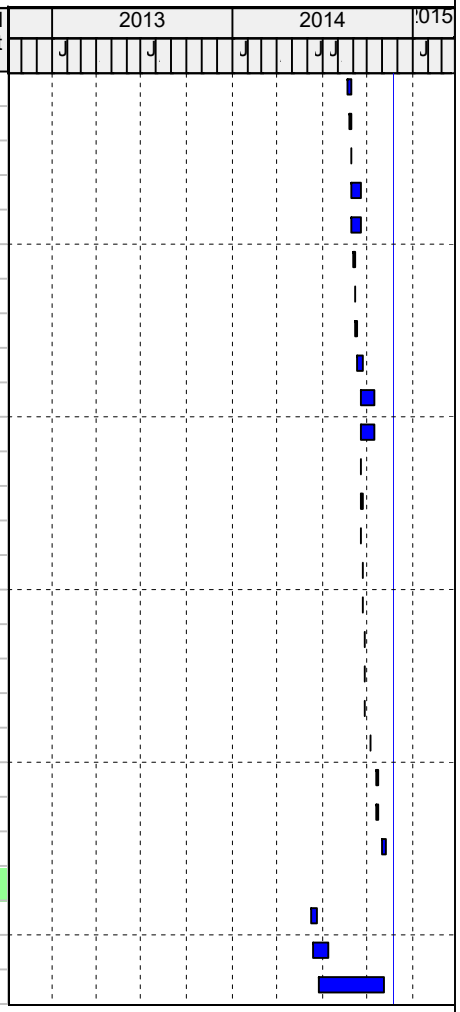



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-6002 | PH - Layout | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| PH-6008 | PH - Interior Wall Framing | 3 | 0 | 24-Jul-14 A | 08-Aug-14 A | |
| PH-6020 | PH - H Mtl Frames | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| PH-6012 | PH - Fire Sprinkler Rl | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |
| PH-6018 | PH - HVAC Rl | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |
| PH-6016 | PH - Electrical Rl | 10 | 0 | 23-Sep-14 A | 14-Nov-14 A | |
| PH-6022 | PH - Fire Alarm / Elec Specialties Rl | 10 | 0 | 23-Sep-14 A | 14-Nov-14 A | |
| **Finishes** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL4-8100 | LL4 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| LL4-8102 | LL4 - GWB Hang (incl. screw inspection) | 3 | 1 | 27-Oct-14 A | 24-Nov-14 | 47 |
| LL4-8104 | LL4 - Int Painting | 1 | 1 | 02-Dec-14 | 02-Dec-14 | 47 |
| LL4-8122 | LL4 - Plumbing Trim / Finish | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 53 |
| LL4-8108 | LL4 - Elec Trim / Finish | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 53 |
| LL4-8110 | LL4 - HVAC Trim / Finish | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 53 |
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 47 |
| LL4-8118 | LL4 - Elec Specialties Trim / Finish | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 47 |
| LL4-8124 | LL4 - Flooring (VCT) | 3 | 3 | 09-Dec-14 | 11-Dec-14 | 53 |
| LL4-8126 | LL4 - Doors & Hardware | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 53 |
| LL4-8114 | LL4 - Striping / Signage | 5 | 5 | 15-Dec-14 | 19-Dec-14 | 53 |
| LL4-8132 | LL4 - Punch | 3 | 3 | 19-Dec-14 | 23-Dec-14 | 53 |
| LL4-8134 | LL4 - Clean | 3 | 3 | 19-Dec-14 | 23-Dec-14 | 53 |
| LL4-8214 | LL4 - Floor Complete | 0 | 0 | | 23-Dec-14 | 53 |
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |

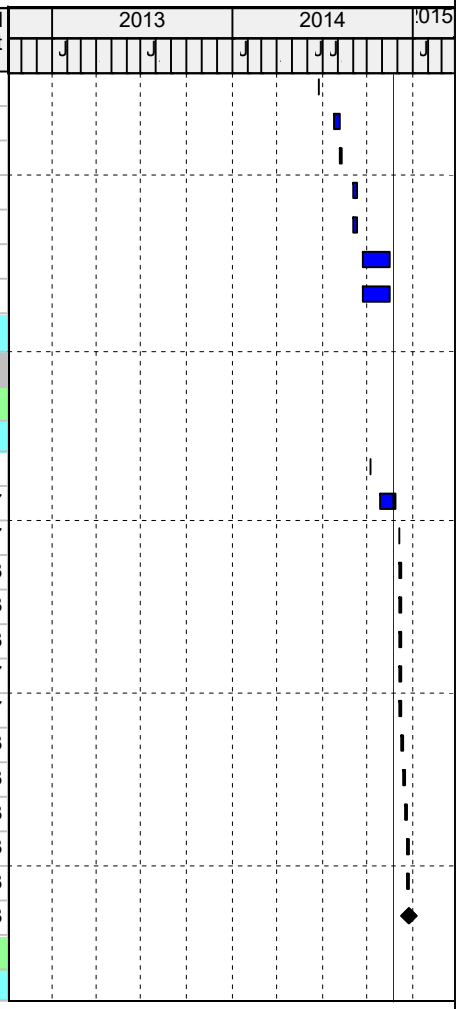



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-8100 | LL3 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| LL3-8102 | LL3 - GWB Hang (incl. screw inspection) | 3 | 1 | 27-Oct-14 A | 24-Nov-14 | 47 |
| LL3-8104 | LL3 - Int Painting | 1 | 1 | 02-Dec-14 | 02-Dec-14 | 47 |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 53 |
| LL3-8108 | LL3 - Elec Trim / Finish | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 53 |
| LL3-8110 | LL3 - HVAC Trim / Finish | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 53 |
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 47 |
| LL3-8118 | LL3 - Elec Specialties Trim / Finish | 2 | 2 | 05-Dec-14 | 08-Dec-14 | 47 |
| LL3-8124 | LL3 - Flooring (VCT) | 3 | 3 | 09-Dec-14 | 11-Dec-14 | 53 |
| LL3-8126 | LL3 - Doors & Hardware | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 53 |
| LL3-8114 | LL3 - Striping / Signage | 5 | 5 | 15-Dec-14 | 19-Dec-14 | 53 |
| LL3-8132 | LL3 - Punch | 3 | 3 | 19-Dec-14 | 23-Dec-14 | 53 |
| LL3-8134 | LL3 - Clean | 3 | 3 | 19-Dec-14 | 23-Dec-14 | 53 |
| LL3-8214 | LL3 - Floor Complete | 0 | 0 | | 23-Dec-14 | 53 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL2E-8102 | LL2 - GWB Hang / Tape / Finish @ Electrical Rooms | 8 | 0 | 24-Jun-14 A | 03-Jul-14 A | |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish & Inspection | 6 | 1 | 16-Sep-14 A | 24-Nov-14 | 58 |
| LL2-8100 | LL2 - Insulation | 5 | 0 | 16-Sep-14 A | 09-Oct-14 A | |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 5 | 0 | 17-Sep-14 A | 27-Oct-14 A | |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| LL2-8136 | LL2 - Chainlink Fencing / Gate @ Recycling | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 54 |
| LL2-8104 | LL2 - Int Painting | 5 | 5 | 25-Nov-14 | 03-Dec-14 | 48 |
| LL2-8122 | LL2 - Plumbing Trim / Finish | 3 | 3 | 02-Dec-14 | 04-Dec-14 | 61 |
| LL2-8108 | LL2 - Elec Trim / Finish | 4 | 4 | 02-Dec-14 | 05-Dec-14 | 70 |
| LL2-8110 | LL2 - HVAC Trim / Finish | 3 | 3 | 02-Dec-14 | 04-Dec-14 | 71 |
| LL2-8112 | LL2 - Fire Sprinkler Trim / Finish | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 50 |

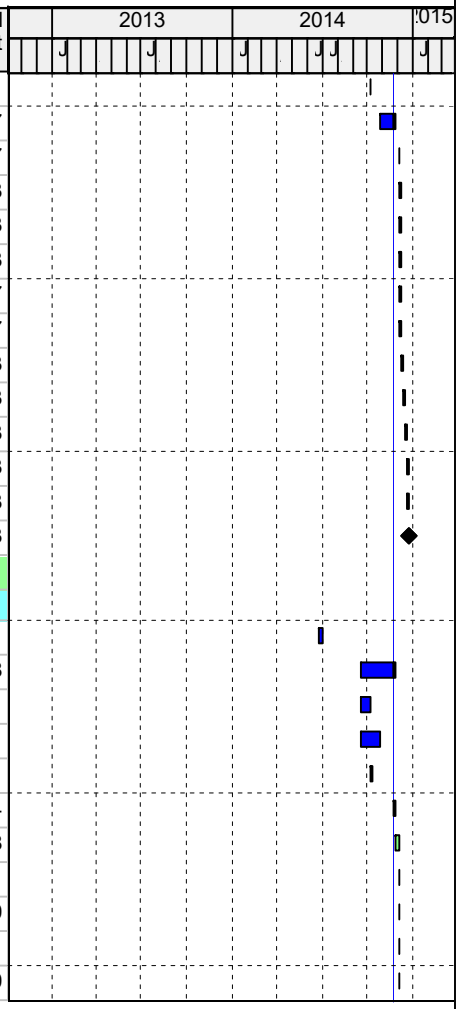



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-8118 | LL2 - Elec Specialties Trim / Finish | 4 | 4 | 02-Dec-14 | 05-Dec-14 | 48 |
| LL2-8128 | LL2 - Entry Gates | 3 | 3 | 02-Dec-14 | 04-Dec-14 | 53 |
| LL2-8116 | LL2 - Finish Carpentry / Millwork | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 60 |
| LL2-8124 | LL2 - Flooring | 5 | 5 | 04-Dec-14 | 10-Dec-14 | 52 |
| LL2-8120 | LL2 - Install Bollards | 3 | 3 | 05-Dec-14 | 09-Dec-14 | 53 |
| LL2-8114 | LL2 - Striping / Signage | 5 | 5 | 11-Dec-14 | 17-Dec-14 | 52 |
| LL2-8126 | LL2 - Doors & Hardware | 4 | 4 | 11-Dec-14 | 16-Dec-14 | 53 |
| LL2-8134 | LL2 - Clean | 5 | 5 | 18-Dec-14 | 24-Dec-14 | 52 |
| LL2-8132 | LL2 - Punch | 5 | 5 | 19-Dec-14 | 29-Dec-14 | 51 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 31-Jul-14 A | |
| LL1-Z2U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 09-May-14 A | |
| LL1-Z3U-8102 | Above Ceiling GWB (At All Areas North of Q-Line) | 5 | 0 | 10-Feb-14 A | 20-Jun-14 A | |
| L1BU-8102 | Above Ceiling GWB [including East Service Corridor] | 5 | 0 | 06-Jun-14 A | 11-Jun-14 A | |
| L1LU-8102 | Above Ceiling GWB | 5 | 0 | 24-Jun-14 A | 13-Oct-14 A | |
| L1KU-8102 | Above Ceiling GWB | 2 | 0 | 26-Jun-14 A | 22-Aug-14 A | |
| LL1-8100 | Insulation | 5 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| LL1-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 28-Jul-14 A | 06-Aug-14 A | |
| LL1-Z2-8102 | GWB Hang (Walls) & Inspection | 4 | 0 | 11-Aug-14 A | 14-Aug-14 A | |
| LL1-Z2-8100 | Insulation | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| LL1-8215 | GWB Tape (Walls) | 10 | 0 | 16-Aug-14 A | 07-Nov-14 A | |
| LL1-Z3-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 15-Sep-14 A | 07-Oct-14 A | |
| LL1-Z3-8100 | Insulation | 5 | 0 | 15-Sep-14 A | 24-Sep-14 A | |
| LL1-Z2-8215 | GWB Tape (Walls/Ceilings) | 7 | 0 | 29-Sep-14 A | 07-Nov-14 A | |
| L1B-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L1K-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |

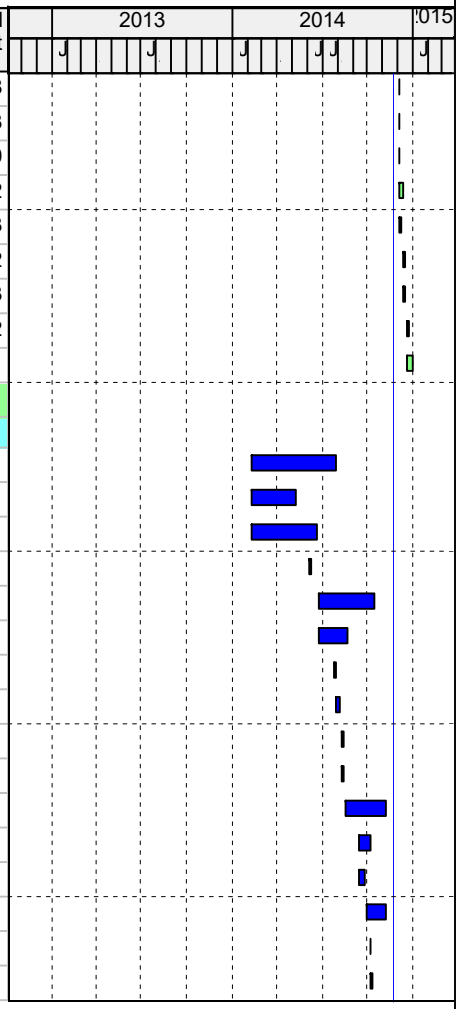



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8215 | GWB Tape (Walls & Ceilings) | 7 | 0 | 07-Oct-14 A | 18-Nov-14 A | |
| L1K-8102 | GWB Hang (Walls) & Inspection | 8 | 0 | 09-Oct-14 A | 31-Oct-14 A | |
| L1L-8100 | Insulation | 4 | 0 | 13-Oct-14 A | 16-Oct-14 A | |
| L1B-8102 | GWB Hang (Walls) & Inspection - Main Ballroom N/S/ | 4 | 0 | 16-Oct-14 A | 22-Oct-14 A | |
| L1L-8102 | GWB Hang (Walls) | 4 | 1 | 30-Oct-14 A | 24-Nov-14 | 1 |
| L1K-8215 | GWB Tape (Walls & Ceilings) | 4 | 0 | 05-Nov-14 A | 18-Nov-14 A | |
| L1B-8215 | GWB Tape (Walls & Ceilings) | 4 | 3 | 06-Nov-14 A | 22-Dec-14 | 15 |
| LL1-8104 | Prime Paint | 5 | 5 | 24-Nov-14 | 02-Dec-14 | 25 |
| LL1-Z3-8104 | Prime Paint | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 25 |
| L1L-8215 | GWB Tape (Walls) | 7 | 7 | 25-Nov-14 | 05-Dec-14 | 5 |
| LL1-Z2-8104 | Prime Paint | 2 | 2 | 01-Dec-14 | 02-Dec-14 | 26 |
| L1K-8104 | Prime Paint | 4 | 4 | 01-Dec-14 | 04-Dec-14 | 14 |
| LL1-8114 | T Bar Grid Ceiling & Inspection | 4 | 4 | 02-Dec-14 | 05-Dec-14 | 25 |
| LL1-Z3-8114 | T Bar Grid Ceiling & Inspection | 4 | 4 | 02-Dec-14 | 05-Dec-14 | 25 |
| LL1-Z2-8114 | T Bar Grid Ceiling & Inspection | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 26 |
| L1K-8106 | Wallcoverings (FRP) | 1 | 1 | 05-Dec-14 | 05-Dec-14 | 14 |
| L1K-8114 | T Bar Grid Ceiling | 4 | 4 | 05-Dec-14 | 10-Dec-14 | 20 |
| LL1-Z2-8124 | Flooring | 5 | 5 | 11-Dec-14 | 17-Dec-14 | 26 |
| LL1-Z2-8106 | Wallcoverings | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 37 |
| LL1-Z3-8124 | Flooring (Epoxy) | 5 | 5 | 13-Dec-14 | 17-Dec-14 | 40 |
| LL1-Z3-8116 | Finish Carpentry / Millwork | 4 | 4 | 17-Dec-14 | 22-Dec-14 | 25 |
| L1K-8140 | Acoustical Ceiling Tile | 4 | 4 | 17-Dec-14 | 22-Dec-14 | 14 |
| LL1-Z2-8116 | Finish Carpentry / Millwork | 5 | 5 | 18-Dec-14 | 24-Dec-14 | 26 |
| L1K-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 19-Dec-14 | 23-Dec-14 | 14 |
| L1K-8124 | Flooring (VCT & Tile) | 3 | 3 | 19-Dec-14 | 23-Dec-14 | 14 |
| L1K-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 19-Dec-14 | 23-Dec-14 | 14 |
| LL1-Z3-8126 | Doors & Hardware | 5 | 5 | 22-Dec-14 | 30-Dec-14 | 25 |

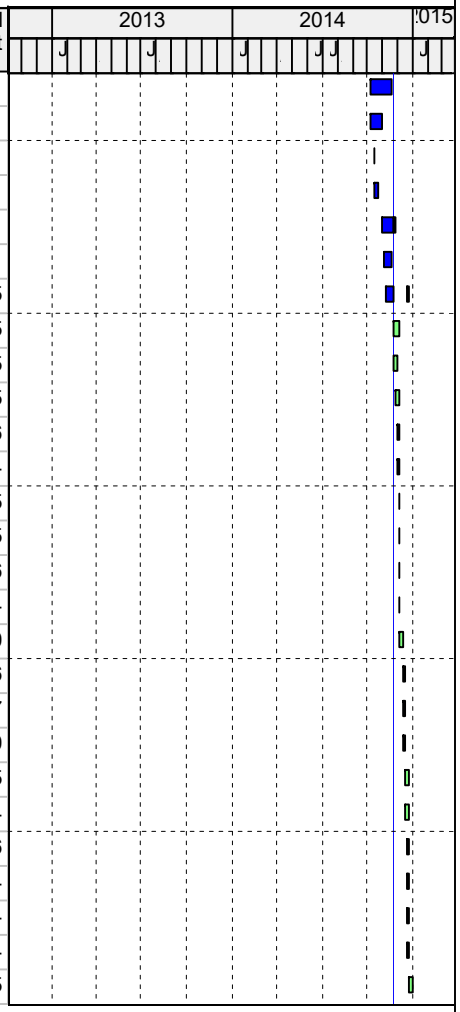



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8104 | Prime Paint | 3 | 3 | 22-Dec-14 | 24-Dec-14 | 0 |
| LL1-8124 | Flooring | 3 | 3 | 23-Dec-14 | 29-Dec-14 | 18 |
| L1B-8104 | Prime Paint | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 15 |
| LL1-Z2-8126 | Doors & Hardware | 3 | 3 | 29-Dec-14 | 31-Dec-14 | 26 |
| L1B-8114 | T Bar Grid Ceiling | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 15 |
| L1L-8114 | Install wood ceiling supports | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 0 |
| LL1-Z3-8140 | Acoustical Ceiling Tile | 3 | 3 | 30-Dec-14 | 02-Jan-15 | 25 |
| LL1-8116 | Finish Carpentry / Millwork | 5 | 5 | 31-Dec-14 | 07-Jan-15 | 18 |
| L1L-8140 | Install wood ceiling | 8 | 8 | 31-Dec-14 | 12-Jan-15 | 0 |
| LL1-Z2-8140 | Acoustical Ceiling Tile | 2 | 2 | 02-Jan-15 | 05-Jan-15 | 26 |
| LL1-Z3-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 02-Jan-15 | 06-Jan-15 | 25 |
| LL1-Z3-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 02-Jan-15 | 06-Jan-15 | 25 |
| L1K-8116 | Finish Carpentry / Millwork | 3 | 3 | 02-Jan-15 | 06-Jan-15 | 15 |
| L1K-8126 | Doors & Hardware | 3 | 3 | 02-Jan-15 | 06-Jan-15 | 15 |
| LL1-Z2-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 05-Jan-15 | 07-Jan-15 | 26 |
| LL1-Z2-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 05-Jan-15 | 07-Jan-15 | 26 |
| L1L-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 05-Jan-15 | 06-Jan-15 | 25 |
| LL1-8126 | Doors & Hardware | 3 | 3 | 06-Jan-15 | 08-Jan-15 | 18 |
| L1B-8124 | Flooring (Carpet) | 4 | 4 | 06-Jan-15 | 09-Jan-15 | 15 |
| LL1-8140 | Acoustical Ceiling Tile | 3 | 3 | 09-Jan-15 | 13-Jan-15 | 18 |
| LL1-Z2-8132 | Punch | 5 | 5 | 12-Jan-15 | 16-Jan-15 | 26 |
| LL1-Z2-8134 | Clean | 5 | 5 | 12-Jan-15 | 16-Jan-15 | 26 |
| L1B-8116 | Finish Carpentry / Millwork | 4 | 4 | 12-Jan-15 | 15-Jan-15 | 18 |
| L1B-8126 | Doors & Hardware | 4 | 4 | 12-Jan-15 | 15-Jan-15 | 18 |
| L1B-8140 | Acoustical Ceiling Tile | 4 | 4 | 12-Jan-15 | 15-Jan-15 | 15 |
| LL1-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 14-Jan-15 | 16-Jan-15 | 18 |
| LL1-Z3-8132 | Punch | 4 | 4 | 14-Jan-15 | 19-Jan-15 | 25 |

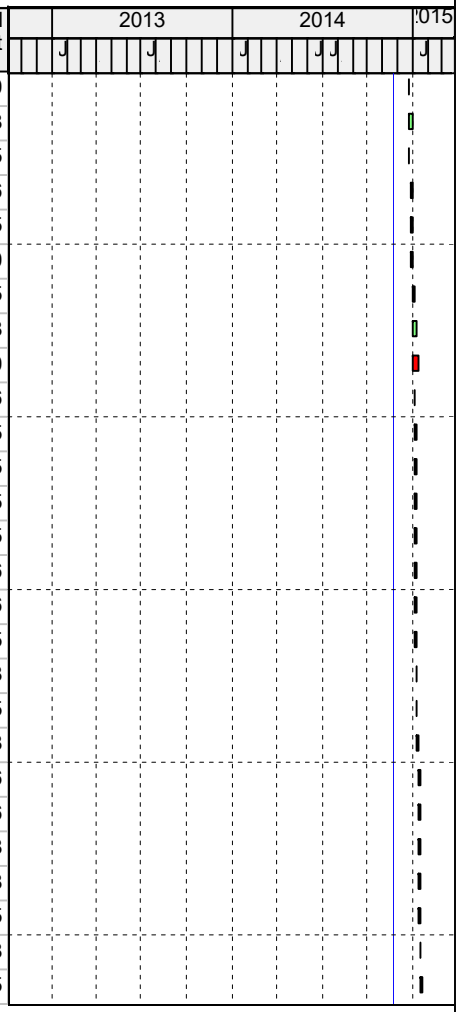



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8134 | Clean | 4 | 4 | 14-Jan-15 | 19-Jan-15 | 25 |
| LL1-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 15-Jan-15 | 19-Jan-15 | 18 |
| L1B-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 15-Jan-15 | 20-Jan-15 | 15 |
| L1B-8118 | Elec & Specialties Trim / Finish | 4 | 4 | 15-Jan-15 | 20-Jan-15 | 15 |
| L1L-8106 | Wallcoverings | 5 | 5 | 20-Jan-15 | 26-Jan-15 | 0 |
| LL1-8132 | Punch | 4 | 4 | 23-Jan-15 | 28-Jan-15 | 18 |
| LL1-8134 | Clean | 4 | 4 | 23-Jan-15 | 28-Jan-15 | 18 |
| L1L-8124 | Flooring | 5 | 5 | 27-Jan-15 | 02-Feb-15 | 0 |
| L1K-8132 | Punch | 5 | 5 | 27-Jan-15 | 02-Feb-15 | 15 |
| L1K-8134 | Clean | 5 | 5 | 27-Jan-15 | 02-Feb-15 | 15 |
| L1B-8132 | Punch | 4 | 4 | 28-Jan-15 | 02-Feb-15 | 15 |
| L1B-8134 | Clean | 4 | 4 | 28-Jan-15 | 02-Feb-15 | 15 |
| L1L-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 4 |
| L1L-8116 | Finish Carpentry / Millwork | 7 | 7 | 03-Feb-15 | 11-Feb-15 | 0 |
| L1L-8126 | Doors & Hardware | 4 | 4 | 05-Feb-15 | 10-Feb-15 | 1 |
| L1L-8132 | Punch | 4 | 4 | 18-Feb-15 | 23-Feb-15 | 0 |
| L1L-8134 | Clean | 4 | 4 | 18-Feb-15 | 23-Feb-15 | 0 |
| **Corridors / Common / Public Areas** | | | | | | |
| LL1-8200 | First Coat Finish Paint | 4 | 4 | 09-Dec-14 | 12-Dec-14 | 25 |
| LL1-Z2-8200 | First Coat Finish Paint | 3 | 3 | 09-Dec-14 | 11-Dec-14 | 26 |
| LL1-Z3-8200 | First Coat Finish Paint | 4 | 4 | 09-Dec-14 | 12-Dec-14 | 25 |
| L1K-8200 | First Coat Finish Paint | 5 | 5 | 11-Dec-14 | 17-Dec-14 | 14 |
| L1K-8204 | HVAC Trim / Finish | 3 | 3 | 19-Dec-14 | 23-Dec-14 | 14 |
| L1B-8200 | First Coat Finish Paint | 3 | 3 | 31-Dec-14 | 05-Jan-15 | 15 |
| LL1-Z3-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 02-Jan-15 | 06-Jan-15 | 25 |
| LL1-Z2-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 05-Jan-15 | 07-Jan-15 | 26 |
| LL1-Z2-8201 | Final Coat Finish Paint | 3 | 3 | 07-Jan-15 | 09-Jan-15 | 26 |

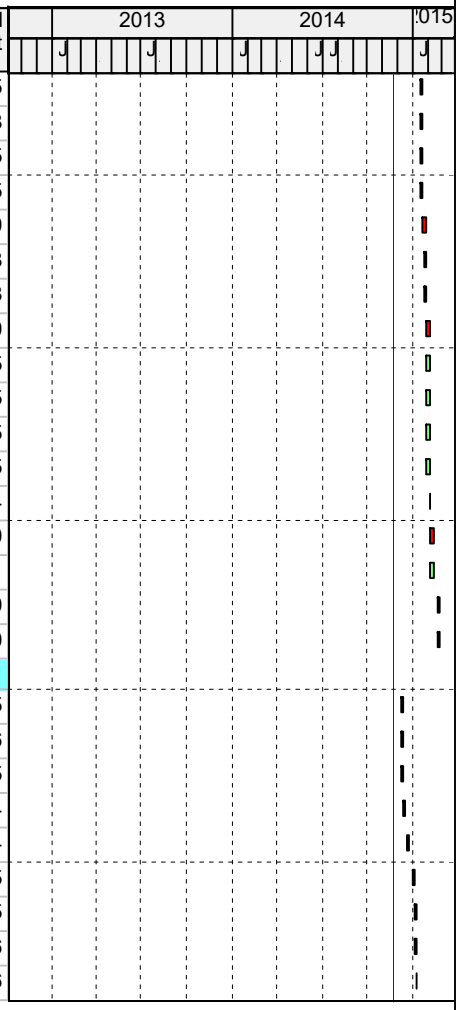



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8201 | Final Coat Finish Paint | 5 | 5 | 07-Jan-15 | 13-Jan-15 | 25 |
| L1K-8201 | Final Coat Finish Paint | 4 | 4 | 07-Jan-15 | 12-Jan-15 | 15 |
| L1L-8200 | First Coat Finish Paint | 5 | 5 | 13-Jan-15 | 19-Jan-15 | 0 |
| L1B-8204 | Mech Trim / Finish (HVAC & Plumbing) | 4 | 4 | 15-Jan-15 | 20-Jan-15 | 15 |
| LL1-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 16-Jan-15 | 20-Jan-15 | 18 |
| LL1-Z2-8214 | LL1 Zone 2 Compllete | 0 | 0 | | 16-Jan-15 | 26 |
| LL1-8201 | Final Coat Finish Paint | 4 | 4 | 19-Jan-15 | 22-Jan-15 | 18 |
| LL1-Z3-8214 | LL1, Zone 3 Complete | 0 | 0 | | 19-Jan-15 | 25 |
| L1B-8201 | Final Coat Finish Paint | 5 | 5 | 21-Jan-15 | 27-Jan-15 | 15 |
| LL1-8214 | LL1, Zone 1 Complete | 0 | 0 | | 28-Jan-15 | 18 |
| L1B-8214 | L1, Zone 2 Complete | 0 | 0 | | 02-Feb-15 | 15 |
| L1K-8214 | L1, Zone 1 Complete | 0 | 0 | | 02-Feb-15 | 15 |
| L1L-8204 | Mech Trim / Finish (HVAC & Plumbing) | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 4 |
| L1L-8201 | Final Coat Finish Paint | 5 | 5 | 11-Feb-15 | 17-Feb-15 | 0 |
| L1L-8214 | L1, Zone 4 Complete | 0 | 0 | | 23-Feb-15 | 0 |
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8100 | L2 - Insulation - North Half | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L02-8102 | L2 - GWB Hang / Tape / Finish - North Half | 7 | 5 | 23-Oct-14 A | 02-Dec-14 | 25 |
| L02-8104 | L2 - Int Painting - North Half | 3 | 3 | 03-Dec-14 | 05-Dec-14 | 25 |
| L02-8106 | L2 - Wallcoverings | 4 | 4 | 08-Dec-14 | 11-Dec-14 | 19 |
| L02-8124 | L2 - Flooring | 5 | 5 | 12-Dec-14 | 18-Dec-14 | 19 |
| L02-8108 | L2 - Elec Trim / Finish | 5 | 5 | 15-Dec-14 | 19-Dec-14 | 25 |
| L02-8110 | L2 - HVAC Trim / Finish | 5 | 5 | 15-Dec-14 | 19-Dec-14 | 25 |
| L02-8112 | L2 - Fire Sprinkler Trim / Finish | 5 | 5 | 15-Dec-14 | 19-Dec-14 | 25 |
| L02-8118 | L2 - Elec Specialties Trim / Finish | 5 | 5 | 15-Dec-14 | 19-Dec-14 | 25 |
| L02-8116 | L2 - Finish Carpentry / Millwork | 4 | 4 | 18-Dec-14 | 23-Dec-14 | 19 |

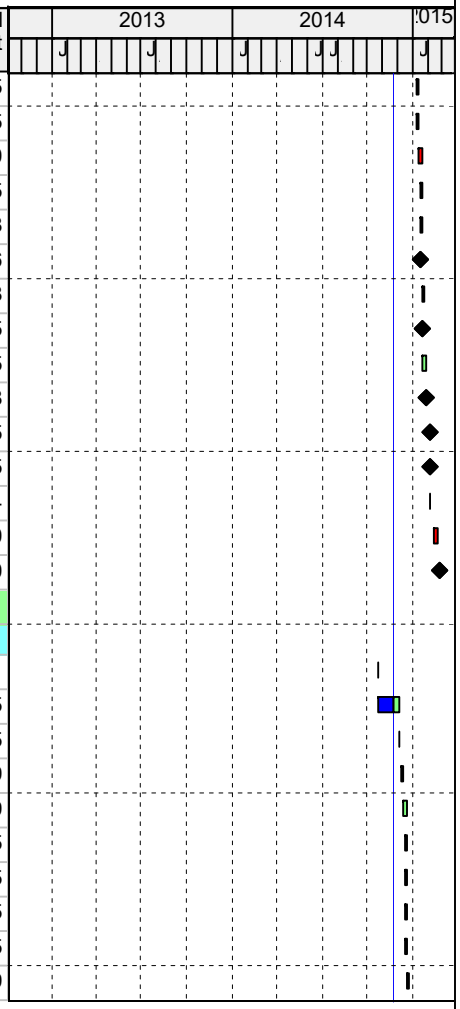



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8120 | L2 - Ceramic Tile / Counter Tops | 5 | 5 | 18-Dec-14 | 24-Dec-14 | 19 |
| L02-8128 | L2 - Bath Specialties | 4 | 4 | 18-Dec-14 | 23-Dec-14 | 25 |
| L02-8122 | L2 - Plumbing Trim / Finish | 5 | 5 | 22-Dec-14 | 30-Dec-14 | 27 |
| L02-8126 | L2 - Doors & Hardware | 5 | 5 | 24-Dec-14 | 02-Jan-15 | 20 |
| L02-8136 | L2 - Lockers / Benches @ Locker Rooms | 5 | 5 | 29-Dec-14 | 05-Jan-15 | 19 |
| L02-8132 | L2 - Punch | 5 | 5 | 13-Jan-15 | 19-Jan-15 | 19 |
| L02-8134 | L2 - Clean | 5 | 5 | 13-Jan-15 | 19-Jan-15 | 19 |
| **Corridors** | | | | | | |
| L02-8200 | L2 - Final Paint @ Common / Public Areas | 5 | 5 | 06-Jan-15 | 12-Jan-15 | 19 |
| L02-8114 | L2 - Signage | 3 | 3 | 13-Jan-15 | 15-Jan-15 | 27 |
| L02-8210 | L2 - Owner Walk / Create Punchlist | 1 | 1 | 20-Jan-15 | 20-Jan-15 | 19 |
| L02-8212 | L2 - Resolve Final Punchlist | 5 | 5 | 21-Jan-15 | 27-Jan-15 | 19 |
| L02-8214 | Floor Complete | 0 | 0 | | 27-Jan-15 | 19 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L03-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L04-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L05-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L06-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L07-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L08-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L09-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L10-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L11-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L12-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L14-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |

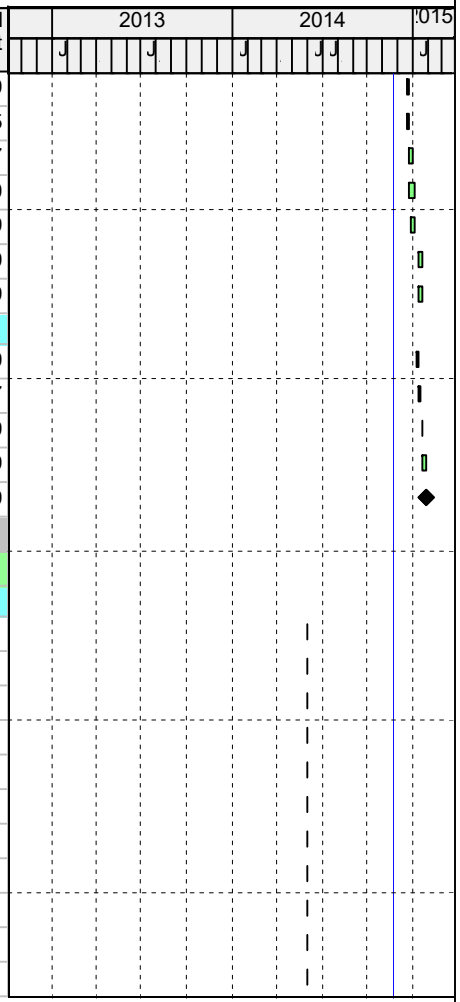



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L16-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L17-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L03-8102S | Stock GWB | 2 | 0 | 27-Jun-14 A | 08-Jul-14 A | |
| L04-8102 | Hang GWB & Inspection | 4 | 0 | 07-Jul-14 A | 16-Jul-14 A | |
| L04-8102S | Stock GWB | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-8102 | Hang GWB & Inspection | 5 | 0 | 09-Jul-14 A | 22-Jul-14 A | |
| L05-8102S | Stock GWB | 2 | 0 | 10-Jul-14 A | 14-Jul-14 A | |
| L05-8102 | Hang GWB & Inspection | 4 | 0 | 17-Jul-14 A | 23-Jul-14 A | |
| L06-8102S | Stock GWB | 2 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L04-8104 | Paint (Prime) | 2 | 0 | 28-Jul-14 A | 05-Aug-14 A | |
| L03-8104 | Paint (Prime) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L03-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L07-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L08-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L06-8102 | Hang GWB & Inspection | 5 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L07-8102 | Hang GWB & Inspection | 6 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L04-8105 | Paint (First Coat & Ceilings) | 5 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L05-8104 | Paint (Prime) | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| L09-8102S | Stock GWB | 2 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 07-Aug-14 A | 11-Aug-14 A | |
| L09-8102 | Hang GWB & Inspection | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| L08-8102 | Hang GWB & Inspection | 6 | 0 | 11-Aug-14 A | 15-Aug-14 A | |
| L06-8104 | Paint (Prime) | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L10-8102S | Stock GWB | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-8102 | Hang GWB & Inspection | 4 | 0 | 13-Aug-14 A | 18-Aug-14 A | |
| L06-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 14-Aug-14 A | 18-Aug-14 A | |

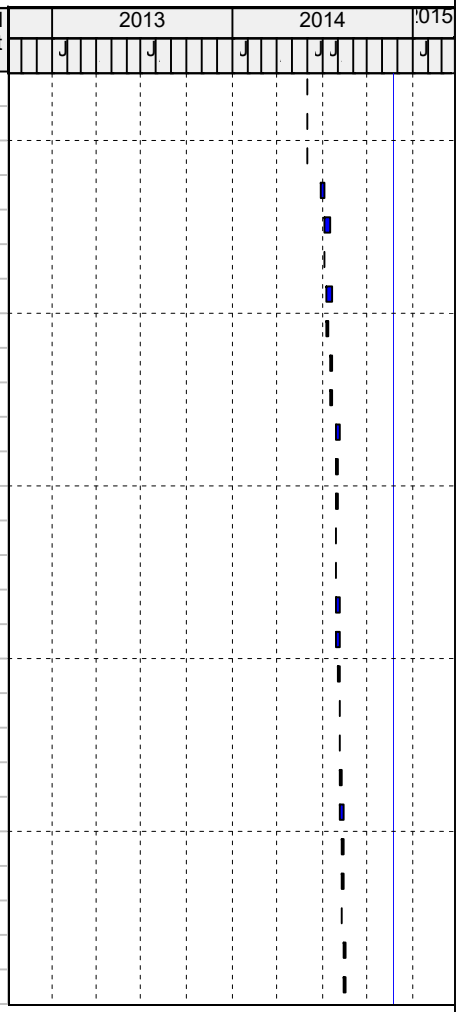



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8102S | Stock GWB | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L07-8104 | Paint (Prime) | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L11-8102 | Hang GWB & Inspection | 4 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| L07-8105 | Paint (First Coat & Ceilings) | 4 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L09-8104 | Paint (Prime) | 2 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L08-8104 | Paint (Prime) | 2 | 0 | 22-Aug-14 A | 25-Aug-14 A | |
| L12-8102 | Hang GWB & Inspection | 4 | 0 | 22-Aug-14 A | 30-Aug-14 A | |
| L12-8102S | Stock GWB | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8108 | Elec Trim / Finish | 4 | 0 | 25-Aug-14 A | 04-Sep-14 A | |
| L08-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L03-8118 | Fire Alarm Trim / Finish | 3 | 0 | 27-Aug-14 A | 29-Sep-14 A | |
| L14-8102S | Stock GWB | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L09-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 29-Aug-14 A | 09-Sep-14 A | |
| L14-8102 | Hang GWB & Inspection | 5 | 0 | 29-Aug-14 A | 05-Sep-14 A | |
| L03-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 02-Sep-14 A | 05-Sep-14 A | |
| L04-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 04-Sep-14 A | 09-Sep-14 A | |
| L10-8104 | Paint (Prime) | 2 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| L15-8102S | Stock GWB | 1 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L15-8102 | Hang GWB & Inspection | 5 | 0 | 06-Sep-14 A | 12-Sep-14 A | |
| L03-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8108 | Elec Trim / Finish | 4 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L04-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 11-Sep-14 A | |
| L05-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 08-Sep-14 A | 12-Sep-14 A | |
| L10-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 08-Sep-14 A | 12-Sep-14 A | |
| L11-8104 | Paint (Prime) | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L04-8116 | Install Base at Guestrooms | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |

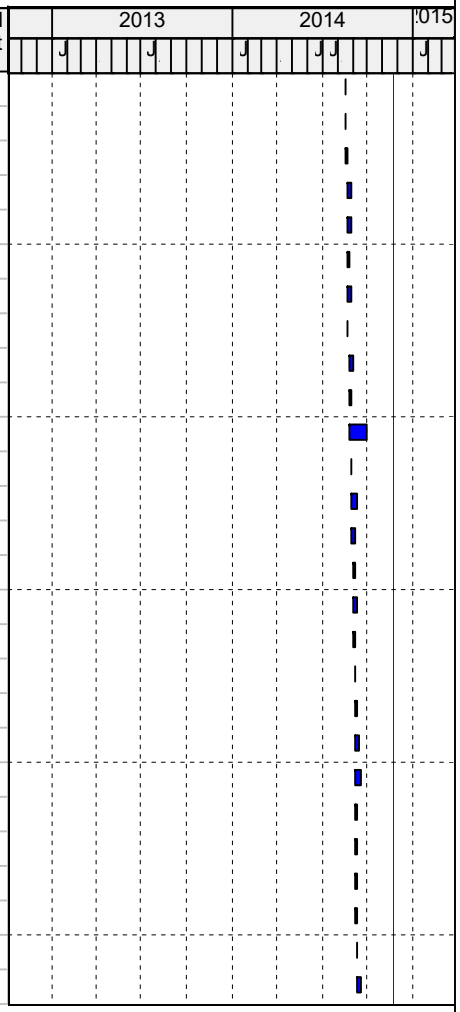



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 10-Sep-14 A | 22-Sep-14 A | |
| L03-8116 | Install Base at Guestrooms | 5 | 0 | 12-Sep-14 A | 16-Sep-14 A | |
| L12-8104 | Paint (Prime) | 2 | 0 | 12-Sep-14 A | 17-Sep-14 A | |
| L05-8116 | Install Base at Guestrooms | 5 | 0 | 16-Sep-14 A | 24-Sep-14 A | |
| L06-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L05-8108 | Elec Trim / Finish | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L07-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 17-Sep-14 A | 23-Sep-14 A | |
| L12-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 17-Sep-14 A | 06-Oct-14 A | |
| L06-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L07-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L14-8104 | Paint (Prime) | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L06-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L06-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L08-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L14-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 24-Sep-14 A | 06-Oct-14 A | |
| L15-8104 | Paint (Prime) | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L03-8110 | HVAC Grilles & Registers | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L03-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8118 | Fire Alarm Trim / Finish | 3 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L10-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L08-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 30-Sep-14 A | 06-Oct-14 A | |
| L03-8126 | Install Doors | 3 | 0 | 01-Oct-14 A | 07-Oct-14 A | |
| L03-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 01-Oct-14 A | 28-Oct-14 A | |
| L04-8126 | Install Doors | 3 | 0 | 02-Oct-14 A | 09-Oct-14 A | |

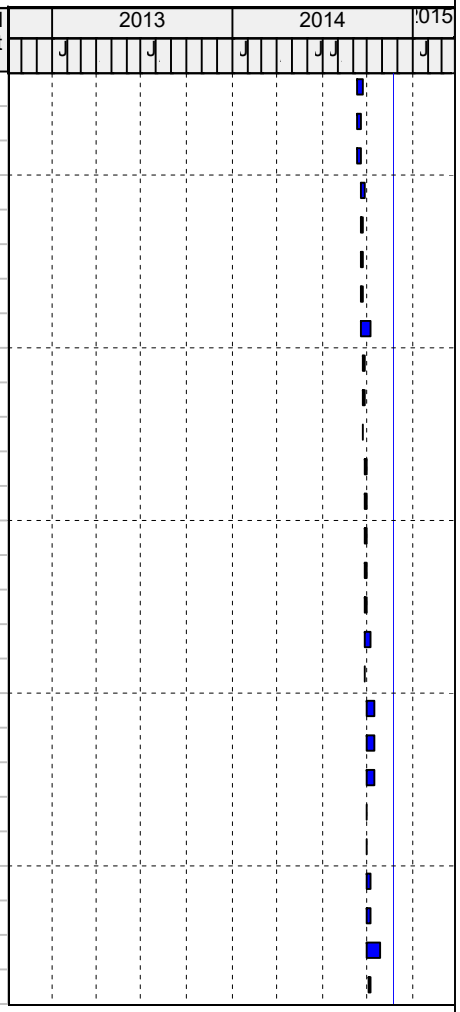



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8116 | Install Base at Guestrooms | 5 | 0 | 02-Oct-14 A | 08-Oct-14 A | |
| L04-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8118 | Fire Alarm Trim / Finish | 3 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8108 | Elec Trim / Finish | 4 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L15-8105 | Paint - First Coast & Ceilings | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8126 | Install Doors | 3 | 0 | 08-Oct-14 A | 10-Oct-14 A | |
| L09-8116 | Install Base and Door Thresholds | 5 | 0 | 08-Oct-14 A | 15-Oct-14 A | |
| L09-8124 | Install Flooring | 5 | 0 | 08-Oct-14 A | 14-Oct-14 A | |
| L16-8102S | Stock GWB | 1 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L09-8112 | Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 10-Oct-14 A | |
| L16-8102 | Hang GWB & Inspection | 4 | 0 | 10-Oct-14 A | 17-Oct-14 A | |
| L06-8118 | Fire Alarm Trim / Finish | 3 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L09-8108 | Lighting and Electrical Trim | 3 | 0 | 13-Oct-14 A | 15-Oct-14 A | |
| L10-8124 | Install Flooring | 5 | 0 | 13-Oct-14 A | 16-Oct-14 A | |
| L11-8112 | Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L03-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 14-Oct-14 A | 04-Nov-14 A | |
| L06-8110 | HVAC Grilles & Registers | 2 | 0 | 14-Oct-14 A | 21-Oct-14 A | |
| L06-8126 | Install Doors | 2 | 0 | 14-Oct-14 A | 20-Oct-14 A | |
| L07-8118 | Fire Alarm Trim / Finish | 3 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L12-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L14-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L08-8118 | Fire Alarm Trim / Finish | 3 | 0 | 15-Oct-14 A | 16-Oct-14 A | |
| L10-8116 | Install Base and Door Thresholds | 5 | 0 | 15-Oct-14 A | 23-Oct-14 A | |
| L15-8112 | Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 16-Oct-14 A | |
| L04-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 16-Oct-14 A | 11-Nov-14 A | |
| L11-8124 | Install Flooring | 5 | 0 | 16-Oct-14 A | 22-Oct-14 A | |

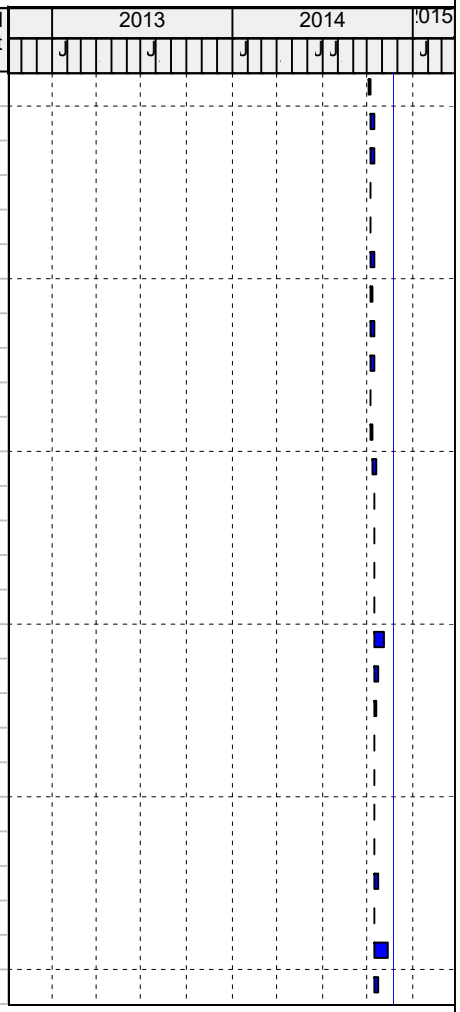



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8102S | Stock GWB | 1 | 0 | 17-Oct-14 A | 17-Oct-14 A | |
| L07-8126 | Install Doors | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |
| L09-8118 | Fire Alarm Trim | 2 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| L05-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 21-Oct-14 A | 14-Nov-14 A | |
| L08-8126 | Install Doors | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L10-8118 | Fire Alarm Trim | 2 | 0 | 21-Oct-14 A | 21-Oct-14 A | |
| L09-8126 | Install Doors | 2 | 0 | 22-Oct-14 A | 23-Oct-14 A | |
| L11-8118 | Fire Alarm Trim | 2 | 0 | 22-Oct-14 A | 22-Oct-14 A | |
| L06-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 23-Oct-14 A | 19-Nov-14 A | |
| L10-8126 | Install Doors | 2 | 0 | 23-Oct-14 A | 27-Oct-14 A | |
| L12-8124 | Install Flooring | 5 | 0 | 23-Oct-14 A | 29-Oct-14 A | |
| L12-8118 | Fire Alarm Trim | 2 | 0 | 23-Oct-14 A | 23-Oct-14 A | |
| L11-8116 | Install Base and Door Thresholds | 5 | 2 | 24-Oct-14 A | 25-Nov-14 | 21 |
| L07-8110 | HVAC Grilles & Registers | 2 | 0 | 27-Oct-14 A | 28-Oct-14 A | |
| L10-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |
| L11-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |
| L17-8102 | Hang GWB & Inspection | 4 | 0 | 27-Oct-14 A | 03-Nov-14 A | |
| L07-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 2 | 28-Oct-14 A | 26-Nov-14 | 43 |
| L08-8120 | Bathrooms - Install Countertops | 3 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L11-8126 | Install Doors | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L12-8108 | Lighting and Electrical Trim | 3 | 0 | 28-Oct-14 A | 30-Oct-14 A | |
| L12-8116 | Install Base and Door Thresholds | 5 | 4 | 28-Oct-14 A | 03-Dec-14 | 21 |
| L14-8118 | Fire Alarm Trim | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L05-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Oct-14 A | 31-Oct-14 A | |
| L06-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Oct-14 A | 31-Oct-14 A | |
| L12-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L14-8108 | Lighting and Electrical Trim | 3 | 0 | 29-Oct-14 A | 03-Nov-14 A | |

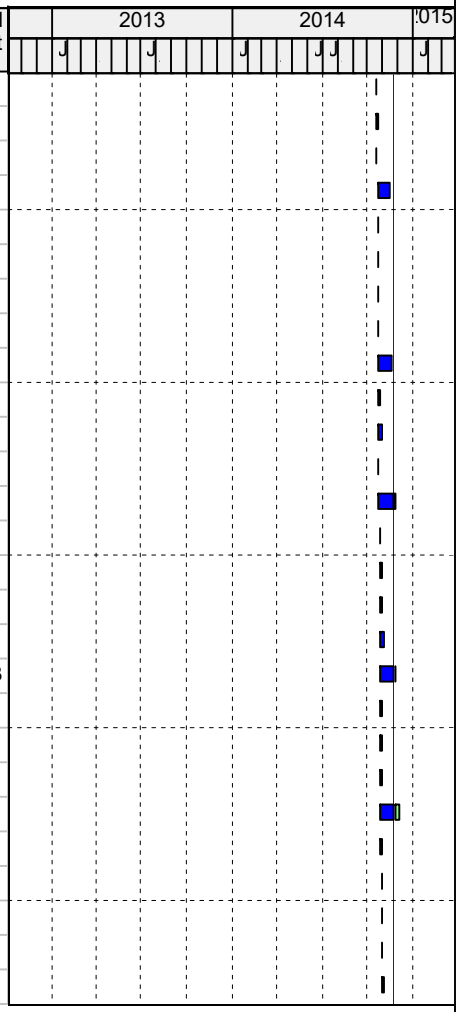



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8118 | Fire Alarm Trim | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L04-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 30-Oct-14 A | 04-Nov-14 A | |
| L07-8120 | Bathrooms - Install Countertops | 3 | 0 | 03-Nov-14 A | 05-Nov-14 A | |
| L08-8110 | HVAC Grilles & Registers | 2 | 0 | 03-Nov-14 A | 04-Nov-14 A | |
| L09-8120 | Bathrooms - Install Countertops | 3 | 0 | 03-Nov-14 A | 05-Nov-14 A | |
| L10-8120 | Bathrooms - Install Countertops | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| L15-8108 | Lighting and Electrical Trim | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| L11-8120 | Bathrooms - Install Countertops | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| L16-8104 | Paint - Prime | 2 | 0 | 05-Nov-14 A | 06-Nov-14 A | |
| L05-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 07-Nov-14 A | 12-Nov-14 A | |
| L16-8105 | Paint - First Coat & Ceilings | 3 | 0 | 07-Nov-14 A | 11-Nov-14 A | |
| L12-8120 | Bathrooms - Install Countertops | 3 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L14-8124 | Install Flooring | 5 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L06-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 13-Nov-14 A | 17-Nov-14 A | |
| L15-8124 | Install Flooring | 5 | 1 | 17-Nov-14 A | 24-Nov-14 | 27 |
| L17-8104 | Paint - Prime | 2 | 0 | 17-Nov-14 A | 18-Nov-14 A | |
| L14-8116 | Install Base and Door Thresholds | 5 | 4 | 18-Nov-14 A | 09-Dec-14 | 21 |
| L16-8126 | Install Doors | 2 | 0 | 18-Nov-14 A | 19-Nov-14 A | |
| L07-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 1 | 19-Nov-14 A | 24-Nov-14 | 43 |
| L15-8116 | Install Base and Door Thresholds | 5 | 4 | 20-Nov-14 A | 09-Dec-14 | 25 |
| L04-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 37 |
| L08-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 38 |
| L09-8110 | HVAC Grilles & Registers | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 45 |
| L09-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 38 |
| L10-8110 | HVAC Grilles & Registers | 2 | 2 | 24-Nov-14 | 25-Nov-14 | 45 |

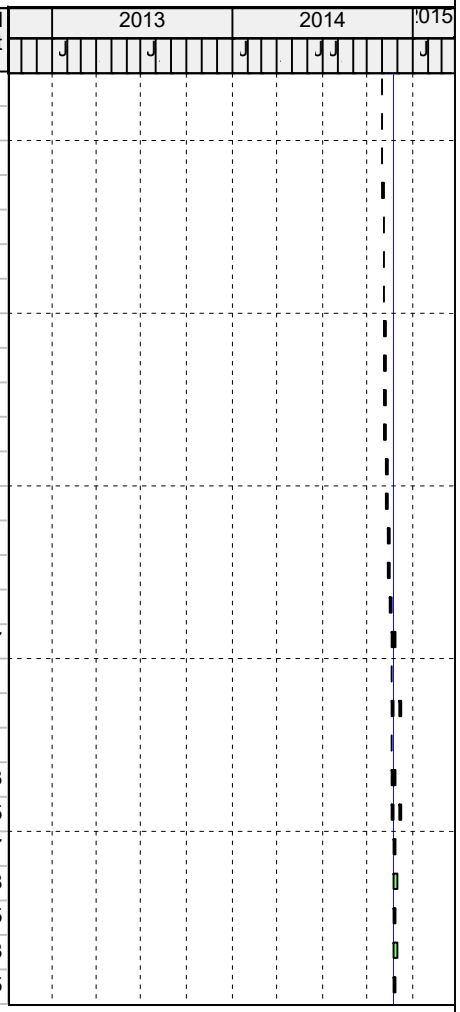



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 38 |
| L11-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 38 |
| L12-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 38 |
| L14-8120 | Bathrooms - Install Countertops | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 32 |
| L15-8120 | Bathrooms - Install Countertops | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 32 |
| L17-8105 | Paint - First Coat & Ceilings | 3 | 3 | 24-Nov-14 | 26-Nov-14 | 24 |
| L03-8107 | Paint Final Coat | 3 | 3 | 25-Nov-14 | 01-Dec-14 | 46 |
| L04-8107 | Paint Final Coat | 3 | 3 | 25-Nov-14 | 01-Dec-14 | 36 |
| L16-8124 | Install Flooring | 5 | 5 | 25-Nov-14 | 03-Dec-14 | 27 |
| L03-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 44 |
| L05-8107 | Paint Final Coat | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 37 |
| L05-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 35 |
| L06-8107 | Paint Final Coat | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 39 |
| L06-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 35 |
| L07-8107 | Paint Final Coat | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 41 |
| L07-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 35 |
| L08-8107 | Paint Final Coat | 3 | 3 | 26-Nov-14 | 02-Dec-14 | 43 |
| L08-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 35 |
| L09-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 35 |
| L10-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 35 |
| L11-8110 | HVAC Grilles & Registers | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 42 |
| L16-8112 | Fire Sprinkler Trim | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 37 |
| L16-8118 | Fire Alarm Trim | 2 | 2 | 26-Nov-14 | 01-Dec-14 | 37 |
| L14-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 01-Dec-14 | 04-Dec-14 | 35 |
| L15-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 01-Dec-14 | 04-Dec-14 | 35 |
| L03-8114 | Signage (By Owner) | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 52 |
| L08-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 02-Dec-14 | 05-Dec-14 | 38 |

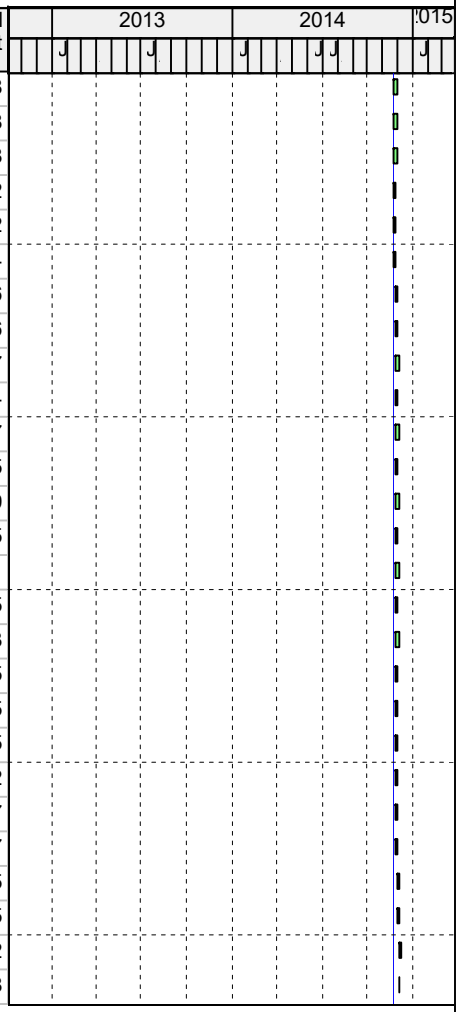



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 02-Dec-14 | 05-Dec-14 | 38 |
| L09-8107 | Paint Final Coat | 3 | 3 | 02-Dec-14 | 04-Dec-14 | 43 |
| L10-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 02-Dec-14 | 05-Dec-14 | 38 |
| L11-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 02-Dec-14 | 05-Dec-14 | 38 |
| L11-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 41 |
| L12-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 02-Dec-14 | 05-Dec-14 | 38 |
| L16-8120 | Bathrooms - Install Countertops | 3 | 3 | 02-Dec-14 | 04-Dec-14 | 31 |
| L10-8107 | Paint Final Coat | 3 | 3 | 04-Dec-14 | 08-Dec-14 | 41 |
| L12-8110 | HVAC Grilles & Registers | 2 | 2 | 04-Dec-14 | 05-Dec-14 | 38 |
| L11-8107 | Paint Final Coat | 3 | 3 | 05-Dec-14 | 09-Dec-14 | 39 |
| L14-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 05-Dec-14 | 10-Dec-14 | 35 |
| L15-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 05-Dec-14 | 10-Dec-14 | 35 |
| L16-8116 | Install Base and Door Thresholds | 5 | 5 | 05-Dec-14 | 11-Dec-14 | 26 |
| L16-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 05-Dec-14 | 10-Dec-14 | 32 |
| L12-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 08-Dec-14 | 09-Dec-14 | 38 |
| L17-8120 | Bathrooms - Install Countertops | 3 | 3 | 09-Dec-14 | 11-Dec-14 | 26 |
| L17-8124 | Install Flooring | 5 | 5 | 09-Dec-14 | 15-Dec-14 | 24 |
| L14-8110 | HVAC Grilles & Registers | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 35 |
| L15-8110 | HVAC Grilles & Registers | 2 | 2 | 10-Dec-14 | 11-Dec-14 | 35 |
| L16-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 11-Dec-14 | 16-Dec-14 | 32 |
| L17-8112 | Fire Sprinkler Trim | 2 | 2 | 11-Dec-14 | 12-Dec-14 | 28 |
| L17-8118 | Fire Alarm Trim | 2 | 2 | 11-Dec-14 | 12-Dec-14 | 28 |
| L12-8107 | Paint Final Coat | 3 | 3 | 12-Dec-14 | 16-Dec-14 | 34 |
| L14-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 34 |
| L15-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 12-Dec-14 | 15-Dec-14 | 34 |
| L16-8108 | Lighting and Electrical Trim | 3 | 3 | 12-Dec-14 | 16-Dec-14 | 30 |
| L17-8116 | Install Base and Door Thresholds | 5 | 5 | 12-Dec-14 | 18-Dec-14 | 24 |

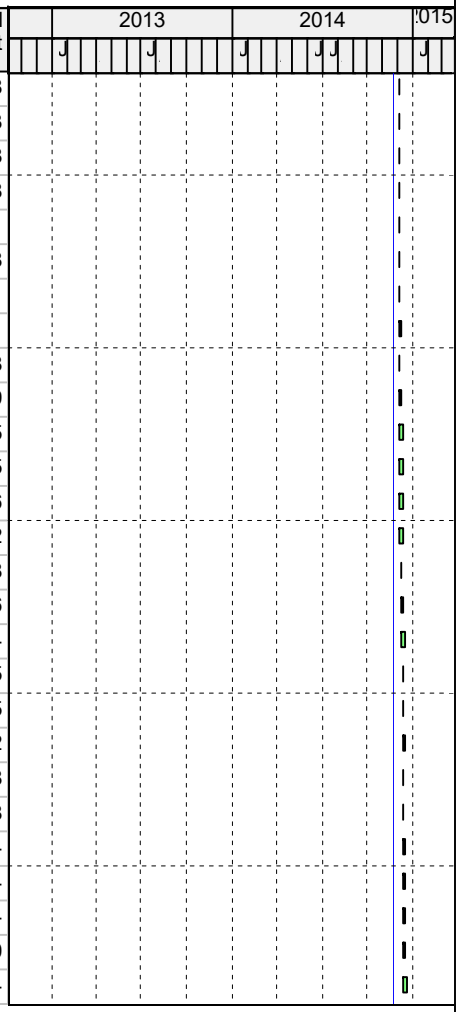



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 12-Dec-14 | 17-Dec-14 | 26 |
| L04-8132 | Punchlist @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 36 |
| L04-8134 | Final Clean @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 36 |
| L05-8132 | Punchlist @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 36 |
| L05-8134 | Final Clean @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 36 |
| L06-8132 | Punchlist @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 36 |
| L06-8134 | Final Clean @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 36 |
| L07-8132 | Punchlist @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 36 |
| L07-8134 | Final Clean @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 36 |
| L08-8132 | Punchlist @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 36 |
| L08-8134 | Final Clean @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 36 |
| L09-8132 | Punchlist @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 36 |
| L09-8134 | Final Clean @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 36 |
| L10-8132 | Punchlist @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 36 |
| L10-8134 | Final Clean @ Guestrooms | 5 | 5 | 16-Dec-14 | 22-Dec-14 | 36 |
| L03-8132 | Punchlist @ Guestrooms | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 35 |
| L03-8134 | Final Clean @ Guestrooms | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 35 |
| L11-8132 | Punchlist @ Guestrooms | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 35 |
| L11-8134 | Final Clean @ Guestrooms | 5 | 5 | 17-Dec-14 | 23-Dec-14 | 35 |
| L16-8110 | HVAC Grilles & Registers | 2 | 2 | 17-Dec-14 | 18-Dec-14 | 31 |
| L12-8132 | Punchlist @ Guestrooms | 5 | 5 | 18-Dec-14 | 24-Dec-14 | 34 |
| L12-8134 | Final Clean @ Guestrooms | 5 | 5 | 18-Dec-14 | 24-Dec-14 | 34 |
| L14-8107 | Paint Final Coat | 3 | 3 | 18-Dec-14 | 22-Dec-14 | 31 |
| L17-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 18-Dec-14 | 23-Dec-14 | 26 |
| L16-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 19-Dec-14 | 22-Dec-14 | 30 |
| L17-8108 | Lighting and Electrical Trim | 3 | 3 | 19-Dec-14 | 23-Dec-14 | 24 |
| L17-8126 | Install Doors | 2 | 2 | 19-Dec-14 | 20-Dec-14 | 32 |

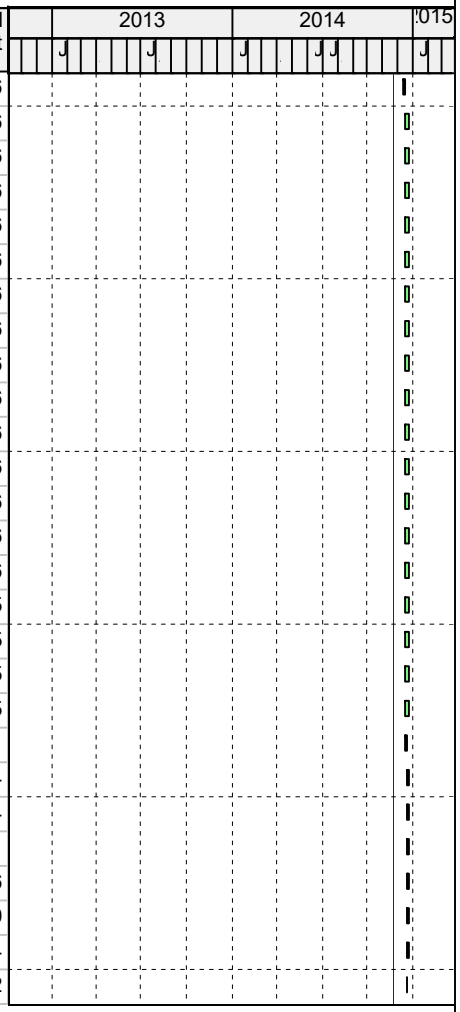


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8132 | Punchlist @ Guestrooms | 5 | 5 | 23-Dec-14 | 31-Dec-14 | 31 |
| L14-8134 | Final Clean @ Guestrooms | 5 | 5 | 23-Dec-14 | 31-Dec-14 | 31 |
| L15-8107 | Paint Final Coat | 3 | 3 | 24-Dec-14 | 30-Dec-14 | 27 |
| L17-8110 | HVAC Grilles & Registers | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 25 |
| L04-8114 | Signage (By Owner) | 5 | 5 | 29-Dec-14 | 06-Jan-15 | 35 |
| L17-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 30-Dec-14 | 31-Dec-14 | 24 |
| L15-8132 | Punchlist @ Guestrooms | 5 | 5 | 31-Dec-14 | 07-Jan-15 | 27 |
| L15-8134 | Final Clean @ Guestrooms | 5 | 5 | 31-Dec-14 | 07-Jan-15 | 27 |
| L16-8107 | Paint Final Coat | 3 | 3 | 02-Jan-15 | 06-Jan-15 | 24 |
| L05-8114 | Signage (By Owner) | 5 | 5 | 05-Jan-15 | 09-Jan-15 | 31 |
| L06-8114 | Signage (By Owner) | 5 | 5 | 07-Jan-15 | 13-Jan-15 | 29 |
| L16-8132 | Punchlist @ Guestrooms | 5 | 5 | 07-Jan-15 | 12-Jan-15 | 29 |
| L16-8134 | Final Clean @ Guestrooms | 5 | 5 | 07-Jan-15 | 12-Jan-15 | 29 |
| L17-8107 | Paint - Final Coat | 3 | 3 | 08-Jan-15 | 12-Jan-15 | 19 |
| L07-8114 | Signage (By Owner) | 5 | 5 | 09-Jan-15 | 15-Jan-15 | 27 |
| L12-8114 | Signage (By Owner) | 5 | 5 | 12-Jan-15 | 19-Jan-15 | 26 |
| L08-8114 | Signage (By Owner) | 5 | 5 | 13-Jan-15 | 19-Jan-15 | 25 |
| L17-8132 | Punchlist @ Guestrooms | 5 | 5 | 13-Jan-15 | 19-Jan-15 | 19 |
| L17-8134 | Final Clean @ Guestrooms | 5 | 5 | 13-Jan-15 | 19-Jan-15 | 19 |
| L11-8114 | Signage (By Owner) | 5 | 5 | 13-Jan-15 | 20-Jan-15 | 25 |
| L14-8114 | Signage (By Owner) | 5 | 5 | 14-Jan-15 | 21-Jan-15 | 24 |
| L15-8114 | Signage (By Owner) | 5 | 5 | 14-Jan-15 | 21-Jan-15 | 24 |
| L09-8114 | Signage (By Owner) | 5 | 5 | 15-Jan-15 | 21-Jan-15 | 23 |
| L16-8114 | Signage (By Owner) | 5 | 5 | 16-Jan-15 | 23-Jan-15 | 22 |
| L17-8114 | Signage (By Owner) | 5 | 5 | 16-Jan-15 | 23-Jan-15 | 22 |
| L10-8114 | Signage (By Owner) | 5 | 5 | 19-Jan-15 | 23-Jan-15 | 21 |
| **Pool Area** | | | | | | |

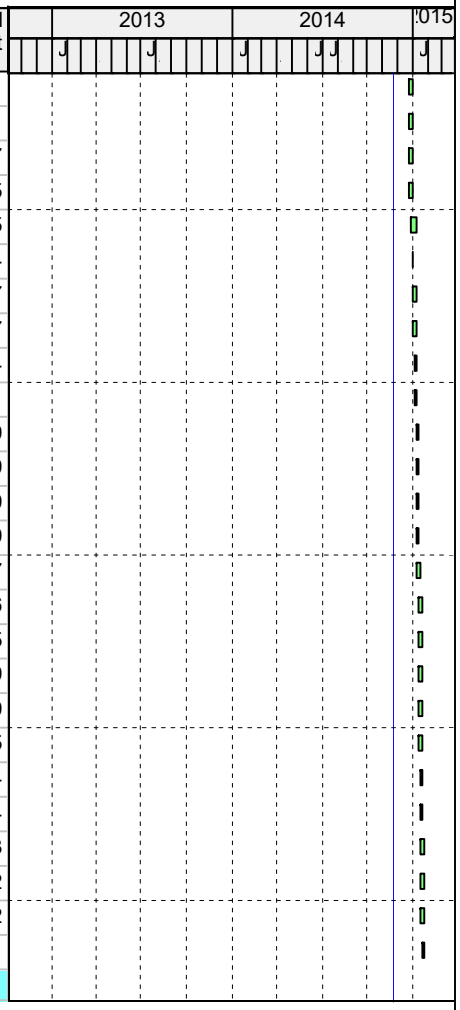



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8216 | L3 Pool - Install tile, coping and depth markers | 5 | 5 | 15-Jan-15 | 21-Jan-15 | 31 |
| **Corridors / Common / Public Areas** | | | | | | |
| L03-8200 | Vinyl Wall Coverings | 3 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L04-8200 | Vinyl Wall Coverings | 5 | 0 | 06-Aug-14 A | 12-Aug-14 A | |
| L05-8200 | Vinyl Wall Coverings | 5 | 0 | 12-Aug-14 A | 22-Sep-14 A | |
| L03-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L06-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L08-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 11-Sep-14 A | 19-Sep-14 A | |
| L04-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| L05-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L06-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L07-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L09-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| L10-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 08-Oct-14 A | |
| L11-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 10-Oct-14 A | |
| L08-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L12-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| L09-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L14-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 16-Oct-14 A | 27-Oct-14 A | |
| L10-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |
| L11-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L15-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 22-Oct-14 A | 29-Oct-14 A | |
| L12-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 03-Nov-14 A | 04-Nov-14 A | |
| L14-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L15-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 05-Nov-14 A | 06-Nov-14 A | |
| L16-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 14-Nov-14 A | 20-Nov-14 A | |

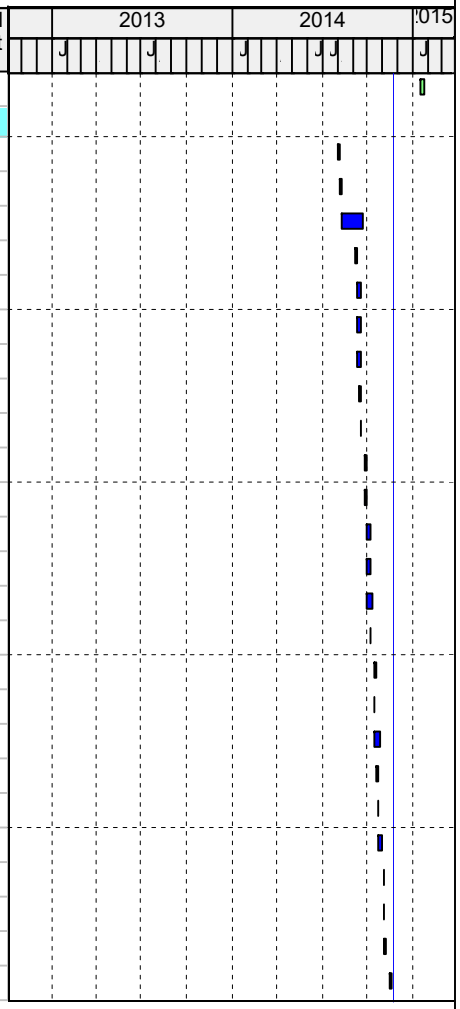



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L17-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 4 | 03-Dec-14 | 08-Dec-14 | 24 |
| L17-8202 | Corridors - Lighting and Electrical Trim | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 24 |
| L04-8206 | Corridors - Flooring & Base | 3 | 3 | 22-Dec-14 | 29-Dec-14 | 22 |
| L05-8206 | Corridors - Flooring & Base | 3 | 3 | 30-Dec-14 | 02-Jan-15 | 20 |
| L04-8208 | Final Clean (Entire Floor) | 2 | 2 | 31-Dec-14 | 05-Jan-15 | 32 |
| L04-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 31-Dec-14 | 02-Jan-15 | 32 |
| L06-8206 | Corridors - Flooring & Base | 3 | 3 | 02-Jan-15 | 06-Jan-15 | 20 |
| L04-8212 | Resolve Final Punchlist | 5 | 5 | 02-Jan-15 | 09-Jan-15 | 32 |
| L05-8208 | Final Clean (Entire Floor) | 2 | 2 | 05-Jan-15 | 07-Jan-15 | 30 |
| L05-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 05-Jan-15 | 06-Jan-15 | 30 |
| L07-8206 | Corridors - Flooring & Base | 3 | 3 | 06-Jan-15 | 08-Jan-15 | 20 |
| L05-8212 | Resolve Final Punchlist | 5 | 5 | 06-Jan-15 | 13-Jan-15 | 30 |
| L06-8208 | Final Clean (Entire Floor) | 2 | 2 | 07-Jan-15 | 09-Jan-15 | 28 |
| L06-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 07-Jan-15 | 08-Jan-15 | 28 |
| L08-8206 | Corridors - Flooring & Base | 3 | 3 | 08-Jan-15 | 12-Jan-15 | 20 |
| L06-8212 | Resolve Final Punchlist | 5 | 5 | 08-Jan-15 | 15-Jan-15 | 28 |
| L11-8206 | Corridors - Flooring & Base | 3 | 3 | 08-Jan-15 | 13-Jan-15 | 21 |
| L12-8206 | Corridors - Flooring & Base | 3 | 3 | 08-Jan-15 | 12-Jan-15 | 25 |
| L04-8214 | Floor Complete | 0 | 0 | | 09-Jan-15 | 32 |
| L07-8208 | Final Clean (Entire Floor) | 2 | 2 | 09-Jan-15 | 13-Jan-15 | 26 |
| L07-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 09-Jan-15 | 12-Jan-15 | 26 |
| L14-8206 | Corridors - Flooring & Base | 3 | 3 | 10-Jan-15 | 14-Jan-15 | 25 |
| L15-8206 | Corridors - Flooring & Base | 3 | 3 | 10-Jan-15 | 14-Jan-15 | 25 |
| L09-8206 | Corridors - Flooring & Base | 3 | 3 | 12-Jan-15 | 14-Jan-15 | 20 |
| L07-8212 | Resolve Final Punchlist | 5 | 5 | 12-Jan-15 | 19-Jan-15 | 26 |
| L05-8214 | Floor Complete | 0 | 0 | | 13-Jan-15 | 30 |

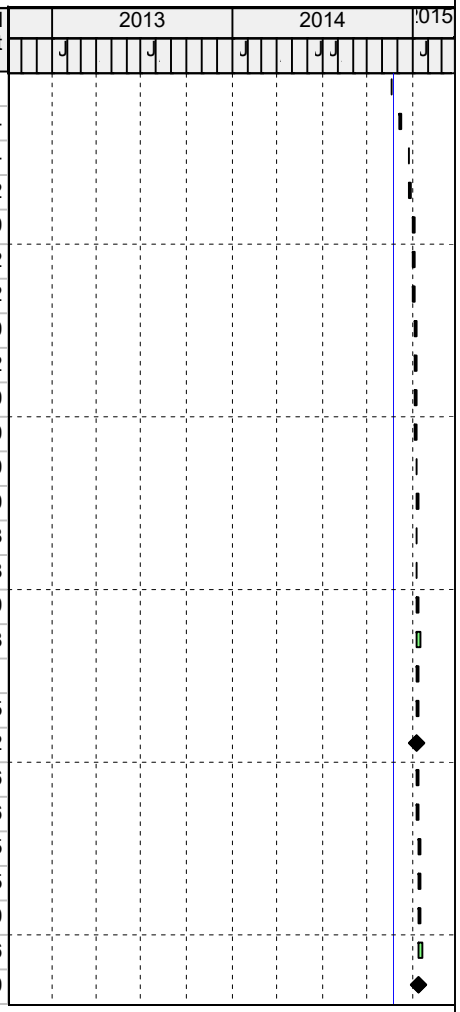



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8208 | Final Clean (Entire Floor) | 2 | 2 | 13-Jan-15 | 15-Jan-15 | 24 |
| L08-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 13-Jan-15 | 14-Jan-15 | 24 |
| L16-8206 | Corridors - Flooring & Base | 3 | 3 | 13-Jan-15 | 16-Jan-15 | 21 |
| L17-8206 | Corridors - Flooring & Base | 3 | 3 | 13-Jan-15 | 16-Jan-15 | 21 |
| L10-8206 | Corridors - Flooring & Base | 3 | 3 | 14-Jan-15 | 16-Jan-15 | 20 |
| L08-8212 | Resolve Final Punchlist | 5 | 5 | 14-Jan-15 | 21-Jan-15 | 24 |
| L11-8208 | Final Clean (Entire Floor) | 2 | 2 | 15-Jan-15 | 16-Jan-15 | 22 |
| L11-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 15-Jan-15 | 15-Jan-15 | 22 |
| L12-8208 | Final Clean (Entire Floor) | 2 | 2 | 15-Jan-15 | 16-Jan-15 | 22 |
| L12-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 15-Jan-15 | 15-Jan-15 | 22 |
| L14-8208 | Final Clean (Entire Floor) | 2 | 2 | 15-Jan-15 | 16-Jan-15 | 22 |
| L14-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 15-Jan-15 | 15-Jan-15 | 22 |
| L06-8214 | Floor Complete | 0 | 0 | | 15-Jan-15 | 28 |
| L09-8208 | Final Clean (Entire Floor) | 2 | 2 | 15-Jan-15 | 19-Jan-15 | 22 |
| L09-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 15-Jan-15 | 16-Jan-15 | 22 |
| L03-8206 | Corridors - Flooring & Base | 3 | 3 | 16-Jan-15 | 19-Jan-15 | 23 |
| L11-8212 | Resolve Final Punchlist | 5 | 5 | 16-Jan-15 | 22-Jan-15 | 22 |
| L12-8212 | Resolve Final Punchlist | 5 | 5 | 16-Jan-15 | 22-Jan-15 | 22 |
| L14-8212 | Resolve Final Punchlist | 5 | 5 | 16-Jan-15 | 22-Jan-15 | 22 |
| L09-8212 | Resolve Final Punchlist | 5 | 5 | 16-Jan-15 | 23-Jan-15 | 22 |
| L15-8208 | Final Clean (Entire Floor) | 2 | 2 | 16-Jan-15 | 20-Jan-15 | 21 |
| L15-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 16-Jan-15 | 19-Jan-15 | 21 |
| L16-8208 | Final Clean (Entire Floor) | 2 | 2 | 16-Jan-15 | 20-Jan-15 | 21 |
| L16-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 16-Jan-15 | 19-Jan-15 | 21 |
| L07-8214 | Floor Complete | 0 | 0 | | 19-Jan-15 | 26 |
| L10-8208 | Final Clean (Entire Floor) | 2 | 2 | 19-Jan-15 | 21-Jan-15 | 20 |
| L10-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 19-Jan-15 | 20-Jan-15 | 20 |

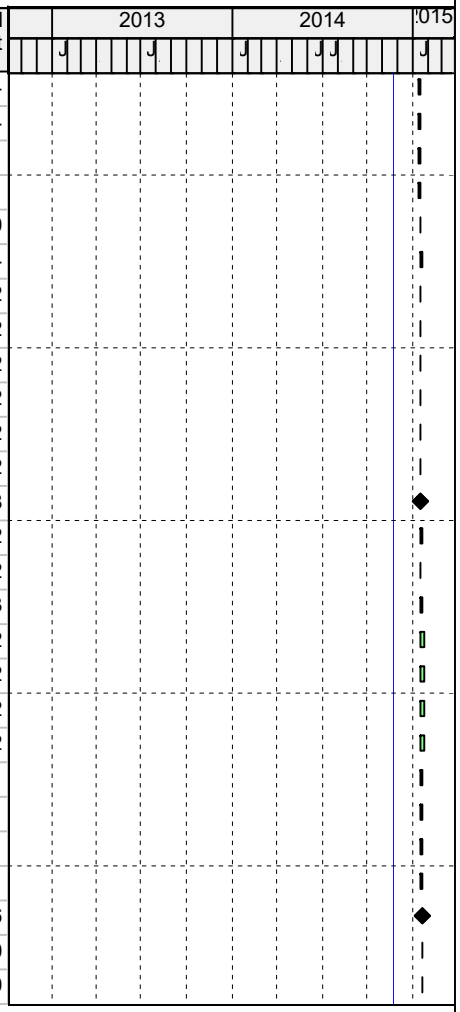



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8212 | Resolve Final Punchlist | 5 | 5 | 19-Jan-15 | 26-Jan-15 | 21 |
| L16-8212 | Resolve Final Punchlist | 5 | 5 | 19-Jan-15 | 26-Jan-15 | 21 |
| L17-8208 | Final Clean (Entire Floor) | 2 | 2 | 20-Jan-15 | 21-Jan-15 | 19 |
| L17-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 20-Jan-15 | 20-Jan-15 | 19 |
| L10-8212 | Resolve Final Punchlist | 5 | 5 | 20-Jan-15 | 27-Jan-15 | 20 |
| L17-8212 | Resolve Final Punchlist | 5 | 5 | 21-Jan-15 | 27-Jan-15 | 19 |
| L08-8214 | Floor Complete | 0 | 0 | | 21-Jan-15 | 24 |
| L11-8214 | Floor Complete | 0 | 0 | | 22-Jan-15 | 22 |
| L12-8214 | Floor Complete | 0 | 0 | | 22-Jan-15 | 22 |
| L14-8214 | Floor Complete | 0 | 0 | | 22-Jan-15 | 22 |
| L09-8214 | Floor Complete | 0 | 0 | | 23-Jan-15 | 22 |
| L15-8214 | Floor Complete | 0 | 0 | | 26-Jan-15 | 21 |
| L16-8214 | Floor Complete | 0 | 0 | | 26-Jan-15 | 21 |
| L10-8214 | Floor Complete | 0 | 0 | | 27-Jan-15 | 20 |
| L17-8214 | Floor Complete | 0 | 0 | | 27-Jan-15 | 19 |
| L03-8208 | Final Clean (Entire Floor) | 2 | 2 | 28-Jan-15 | 29-Jan-15 | 13 |
| L03-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 13 |
| L03-8212 | Resolve Final Punchlist | 5 | 5 | 29-Jan-15 | 04-Feb-15 | 13 |
| L03-8214 | Floor Complete | 0 | 0 | | 04-Feb-15 | 13 |
| **Mech Penthouse** | | | | | | |
| PH-8100 | PH - Insulation & Vapor Barrier | 5 | 0 | 09-Oct-14 A | 13-Oct-14 A | |
| PH-8102 | PH - Complete GWB Hang / Tape / Finish | 6 | 0 | 14-Oct-14 A | 10-Nov-14 A | |
| PH-8104 | PH - Int Painting | 4 | 4 | 24-Nov-14 | 01-Dec-14 | 56 |
| PH-8122 | PH - Plumbing Trim / Finish | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 61 |
| PH-8108 | PH - Elec Trim / Finish | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 56 |
| PH-8110 | PH - HVAC Trim / Finish | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 56 |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 56 |

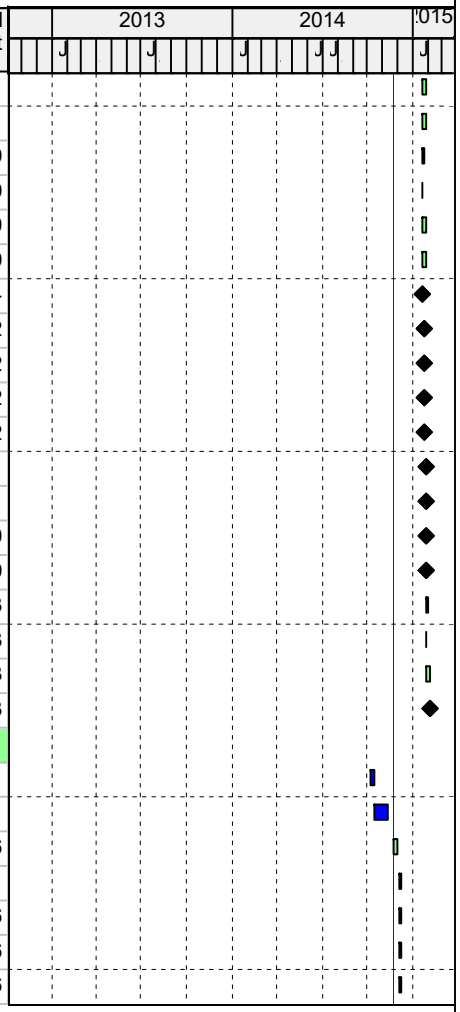



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-8114 | PH - Install Stairs to Roof | 1 | 1 | 02-Dec-14 | 02-Dec-14 | 66 |
| PH-8126 | PH - Doors & Hardware | 2 | 2 | 02-Dec-14 | 03-Dec-14 | 62 |
| PH-8118 | PH - Elec Specialties Trim / Finish | 5 | 5 | 02-Dec-14 | 08-Dec-14 | 56 |
| PH-8124 | PH - Flooring | 5 | 5 | 05-Dec-14 | 11-Dec-14 | 56 |
| PH-8132 | PH - Contractor Pre-Punchlist | 1 | 1 | 12-Dec-14 | 12-Dec-14 | 58 |
| PH-8134 | PH - Final Trims and Touch-Up | 3 | 3 | 12-Dec-14 | 16-Dec-14 | 56 |
| PH-8208 | PH - Final Clean | 1 | 1 | 17-Dec-14 | 17-Dec-14 | 56 |
| PH-8212 | PH - Final Punchlist | 1 | 1 | 18-Dec-14 | 18-Dec-14 | 56 |
| PH-8214 | PH - Floor Complete | 0 | 0 | | 18-Dec-14 | 56 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| **Smoke Control** | | | | | | |
| CO-7104 | Smoke Control Pre-Testing (Podium) | 12 | 12 | 27-Jan-15 | 11-Feb-15 | 15 |
| CO-7106 | City of Bellevue Smoke Control Testing (Podium) | 5 | 5 | 12-Feb-15 | 18-Feb-15 | 15 |
| CO-7108 | Final Marriott Smoke Control Testing | 5 | 5 | 12-Mar-15 | 18-Mar-15 | 0 |
| **Fire Sprinklers** | | | | | | |
| CO-7110 | Fire Sprinkler Pre-Testing (Podium) | 12 | 12 | 27-Jan-15 | 11-Feb-15 | 15 |
| CO-7112 | City of Bellevue Fire Sprinkler Inspection / Approval (F | 5 | 5 | 12-Feb-15 | 18-Feb-15 | 15 |
| CO-7114 | Marriott Fire Sprinkler Testing | 5 | 5 | 19-Feb-15 | 25-Feb-15 | 15 |
| **Fire Alarm** | | | | | | |
| CO-7116 | Fire Alarm Pre-Testing (Podium) | 12 | 12 | 20-Jan-15 | 04-Feb-15 | 20 |
| CO-7118 | City of Bellevue Fire Alarm Inspection / Approval (Pod | 5 | 5 | 10-Feb-15 | 16-Feb-15 | 17 |
| CO-7120 | Marriott Fire Alarm Testing | 5 | 5 | 17-Feb-15 | 23-Feb-15 | 17 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| CO-7100 | Cx - Start-Up - Garage Exhaust Fan and VFD's | 4 | 4 | 01-Dec-14* | 04-Dec-14 | 35 |
| CO-7102 | Cx - DDC Point-To-Point - Garage Exhaust Fans | 5 | 5 | 05-Dec-14 | 11-Dec-14 | 61 |

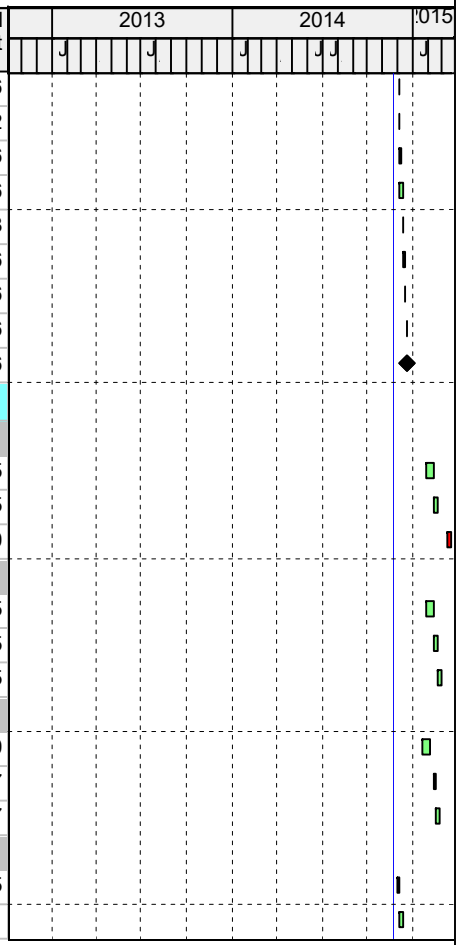



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Working Schedule - 12-21-14 Update** | | | | | | |
| L09-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-04 A | 30-Sep-14 A | |
| I-1500 | Owner release revised LV design - Tower (ASIs 5, 13, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-1550 | Owner release revised LV design - Podium (ASIs 5, 1 | 200 | 0 | 23-May-13 A | 28-Apr-14 A | |
| I-1900 | Owner issue design revisions (ASIs 4, 9, 19, 34) | 215 | 0 | 23-May-13 A | 24-Mar-14 A | |
| I-2500 | Owner issue LL1 electrical revisions (ASIs 7, 9r2, 14, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-3400 | Owner provide Level 2 ceiling heights | 180 | 0 | 24-Jun-13 A | 24-Mar-14 A | |
| I-3700 | Owner resolve wall condition between stair and Eleva | 200 | 0 | 27-Jun-13 A | 16-Jun-14 A | |
| MM-1000 | MM - Temporary Power Available | 0 | 0 | 08-Jul-13 A | | |
| I-2100 | Owner revise roof steel design (Submittals 365, 370, | 200 | 0 | 09-Jul-13 A | 07-Apr-14 A | |
| I-2200 | Owner resolve elevator steel issue (RFI 112, RFI 112. | 200 | 0 | 09-Jul-13 A | 03-Mar-14 A | |
| I-2400 | Owner provide Tower light fixture selections (ASI 36) | 185 | 0 | 18-Jul-13 A | 08-Apr-14 A | |
| I-2900 | Owner revise Food Service and Kitchen (ASIs 11, 12, | 140 | 0 | 08-Aug-13 A | 27-Feb-14 A | |
| I-1400 | Owner develop envelope redesign | 70 | 0 | 27-Aug-13 A | 12-Dec-13 A | |
| I-3600 | Owner closeout glass/glazing allowance | 160 | 0 | 04-Sep-13 A | 30-Apr-14 A | |
| I-1200 | Owner release revised Concierge Lounge design (AS | 160 | 0 | 06-Sep-13 A | 08-Apr-14 A | |
| I-2800 | Owner revise interior public space design (ASIs 16, 18 | 130 | 0 | 25-Sep-13 A | 09-Apr-14 A | |
| I-2000 | Owner approve door frames (Submittals 258, 454, 48 | 85 | 0 | 27-Sep-13 A | 23-Jan-14 A | |
| I-3100 | Owner revise ballroom ceiling design (ASIs 18, 25) | 100 | 0 | 17-Oct-13 A | 25-Feb-14 A | |
| I-1600 | Owner provide directive for south & east corridor encl | 110 | 0 | 28-Oct-13 A | 18-Apr-14 A | |
| I-2300 | Owner resolve fire smoke dampers issue (RFI 233) | 115 | 0 | 30-Oct-13 A | 11-Apr-14 A | |
| I-2600 | Owner resolve L2 slab coordination issue | 4 | 0 | 13-Nov-13 A | 16-Nov-13 A | |
| I-2700 | Owner revise tower guest rooms design (ASIs 23, 29) | 58 | 0 | 04-Dec-13 A | 26-Feb-14 A | |
| I-1700 | Owner provide design for dry site utilities (ASIs 20, 20 | 66 | 0 | 09-Dec-13 A | 13-Mar-14 A | |
| I-1402 | Begin exterior panel production | 41 | 0 | 13-Dec-13 A | 12-Feb-14 A | |
| I-1300 | Owner issue "Hold" directive (email) | 0 | 0 | | 19-Dec-13 A | |
| I-1100 | Owner release revised L17 design (ASI 23, 29R1) | 74 | 0 | 20-Dec-13 A | 08-Apr-14 A | |

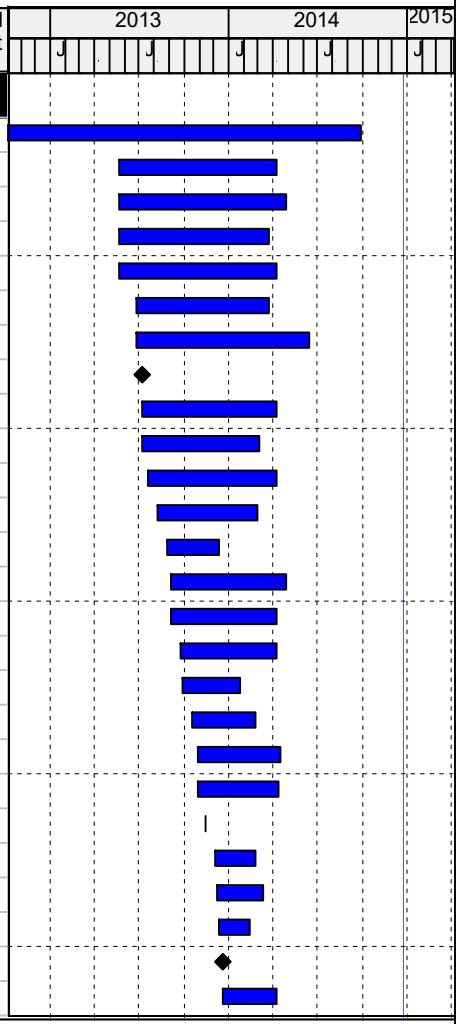


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1302 | Owner issue ASI 30 (Prep Kitchen Revisions) | 47 | 0 | 20-Dec-13 A | 27-Feb-14 A | |
| I-1404 | City of Bellevue Approval | 90 | 0 | 23-Dec-13 A | 15-Jul-14 A | |
| I-3000 | Owner revise bar area (change to straight bar, IDRFI-( | 71 | 0 | 22-Jan-14 A | 27-May-14 A | |
| I-1306 | Prep Kitchen - Additional plumbing (ASI 30) | 4 | 0 | 17-Feb-14 A | 01-Aug-14 A | |
| I-2202 | Fabricate revised elevator steel | 60 | 0 | 04-Mar-14 A | 07-May-14 A | |
| I-2704 | Framing "Go Back" work for ASIs 23, 29 - L4 | 1 | 0 | 05-Mar-14 A | 12-Mar-14 A | |
| I-3900 | RFI 471, Resolve Ballroom parapet height issue | 1 | 0 | 08-Mar-14 A | 07-May-14 A | |
| I-1702 | Owner provide directive to proceed | 26 | 0 | 14-Mar-14 A | 01-May-14 A | |
| I-3300 | Owner provide Guest Room plumbing fixture selectio | 1 | 0 | 20-Mar-14 A | 20-Mar-14 A | |
| I-1902 | Procure revised structural steel | 15 | 0 | 25-Mar-14 A | 14-Apr-14 A | |
| I-4000 | Owner complete design of east stitched enclosure (fo | 1 | 0 | 01-Apr-14 A | 14-May-14 A | |
| I-2102 | Fabricate revised roof steel | 20 | 0 | 08-Apr-14 A | 15-May-14 A | |
| I-3200 | Owner provide light fixture selections for podium level | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| I-3800 | Resolve Heat Pump Electrical Overcurrent Issue | 20 | 0 | 23-Apr-14 A | 18-Jun-14 A | |
| L10-8221 | HVAC Risers Duct Insulation | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L11-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| I-2304 | Framing "Go Back" work at L3 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2306 | Framing "Go Back" work at L4 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2308 | Framing "Go Back" work at L5 for RFI 233 | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2706 | Framing "Go Back" work for ASIs 23, 29 - L5 | 1 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2708 | Framing "Go Back" work for ASIs 23, 29 - L6 | 1 | 0 | 29-Apr-14 A | 09-May-14 A | |
| I-2702 | Framing "Go Back" work for ASIs 23, 29 - L3 | 1 | 0 | 01-May-14 A | 01-May-14 A | |
| I-1706 | PSE scheduling delay | 10 | 0 | 01-May-14 A | 20-May-14 A | |
| I-3602 | Complete shop drawings & fab/deliver storefront fram | 40 | 0 | 01-May-14 A | 14-Jun-14 A | |
| L04-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| I-1802 | Rework framing for door hold-opens - LL4 | 1 | 0 | 07-May-14 A | 08-May-14 A | |

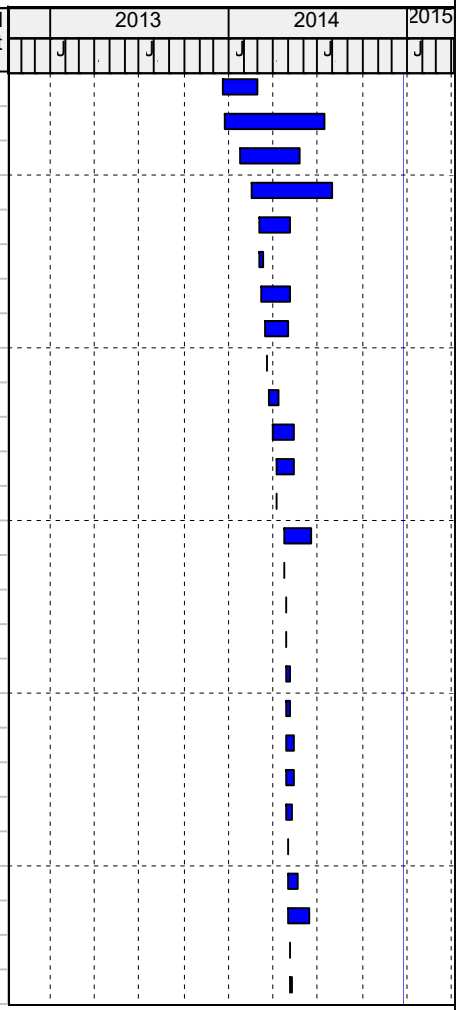


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-May-14 A | 12-May-14 A | |
| I-1800 | Owner issue directive to proceed with door hold-open | 1 | 0 | 08-May-14 A | 08-May-14 A | |
| I-1804 | Rework framing for door hold-opens - LL3 | 1 | 0 | 08-May-14 A | 09-May-14 A | |
| I-2312 | Framing "Go Back" work at L7 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-2314 | Framing "Go Back" work at L8 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-3902 | Install Ballroom parapet extension | 5 | 0 | 08-May-14 A | 13-May-14 A | |
| I-1806 | Rework framing for door hold-opens - LL2 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-1808 | Rework framing for door hold-opens - LL1 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-2310 | Framing "Go Back" work at L6 for RFI 233 | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| I-2710 | Framing "Go Back" work for ASIs 23, 29 - L7 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| L05-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L06-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L05-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| LL2E-8110 | LL2 - Electrical, Fire pumps/equipment final connectic | 5 | 0 | 12-May-14 A | 30-Oct-14 A | |
| PH-8704 | PH - Install Machine Support Steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| PH-8710 | Install elevator rail support steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| L03-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L03-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 13-May-14 A | 14-May-14 A | |
| I-4002 | East Stitched - Install framing and windows | 9 | 0 | 19-May-14 A | 09-Jun-14 A | |
| L10-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L11-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L12-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| RF-4038 | AR - Concrete pads and curbs | 5 | 0 | 21-May-14 A | 04-Jun-14 A | |
| L10-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L11-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L12-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |

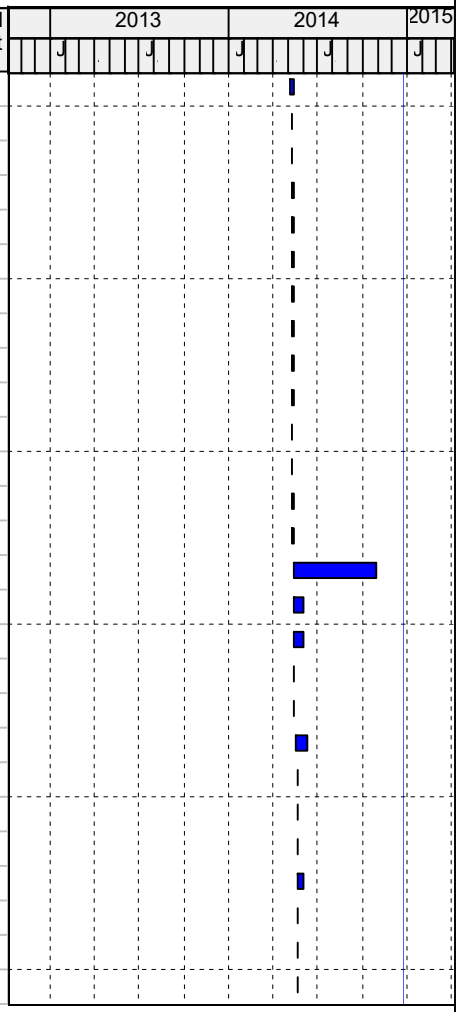



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L15-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 27-May-14 A | |
| L11-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 07-Jun-14 A | |
| L12-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 27-May-14 A | 06-Jun-14 A | |
| I-3002 | City of Bellevue approve bar design changes. | 5 | 2 | 28-May-14 A | 23-Dec-14 | 10 |
| L16-8221 | HVAC Risers Duct Insulation | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| PH-8712 | PH - Complete Framing and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| PH-8714 | Stage PH/L18 roofing materials | 2 | 0 | 30-May-14 A | 30-May-14 A | |
| L08-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L08-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 02-Jun-14 A | 20-Jun-14 A | |
| PH-8704I | Correct support steel embeds | 2 | 0 | 02-Jun-14 A | 11-Jun-14 A | |
| L14-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 03-Jun-14 A | 04-Jun-14 A | |
| L17-8221 | HVAC Risers Duct Insulation | 1 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| PC-4010 | PC - Fireproof Entry Roof Steel | 5 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| I-4100 | Owner resolve trap primers issue (RFI 560) | 5 | 0 | 03-Jun-14 A | 20-Jun-14 A | |
| RF-6028 | Tower Roof - Structural Steel | 5 | 0 | 04-Jun-14 A | 17-Jun-14 A | |
| L14-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L1B-6005 | Head of Wall Fire Caulk at CMU (including East Servi | 2 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L14-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L15-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |

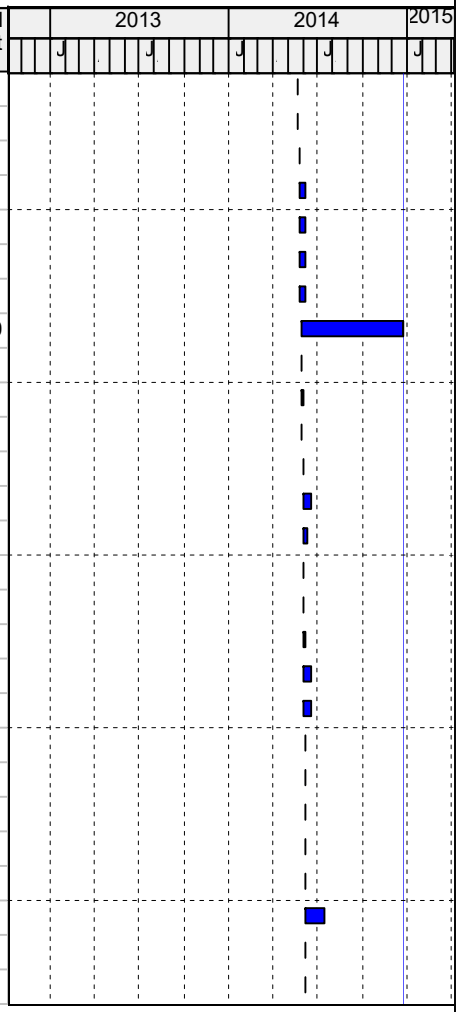



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L09-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 11-Jun-14 A | 12-Jun-14 A | |
| I-3702 | Complete wall framing at Stair/Elevator 5 (LL4) | 2 | 0 | 18-Jun-14 A | 20-Jun-14 A | |
| I-3720 | Fireproof added steel between Stair 1 and Elevator 5 | 5 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| I-3722 | Complete GWB between Stair 1 and Elevator 5 shaft | 10 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| LL1-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 22-Jul-14 A | |
| TC-5912 | Tower Crane pour-backs (LL4 to L3) | 4 | 0 | 19-Jun-14 A | 26-Jun-14 A | |
| LL1-Z2-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL4-6005 | LL4 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| LL3-6005 | LL3 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| L03-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 21-Jun-14 A | 21-Jun-14 A | |
| L06-6040 | Test Heat Pumps - L3, L4, L5 and L6 | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L03-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| L17-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL2-6005 | LL2 - Seismic Head Of Wall Fire Caulk at CMU | 5 | 0 | 24-Jun-14 A | 18-Jul-14 A | |
| I-3704 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL1-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z2-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z3-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 04-Aug-14 A | |
| L1L-6005 | Head of Wall Fire Caulk at CMU (including back of ho | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1K-6005 | Head of Wall Fire Caulk at CMU & Inspection | 2 | 0 | 24-Jun-14 A | 08-Aug-14 A | |
| L03-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L04-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| I-3710 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| I-3712 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| L1K-6018a | Install Kitchen hoods and grease ducts (OFCI) | 10 | 0 | 25-Jun-14 A | 07-Oct-14 A | |

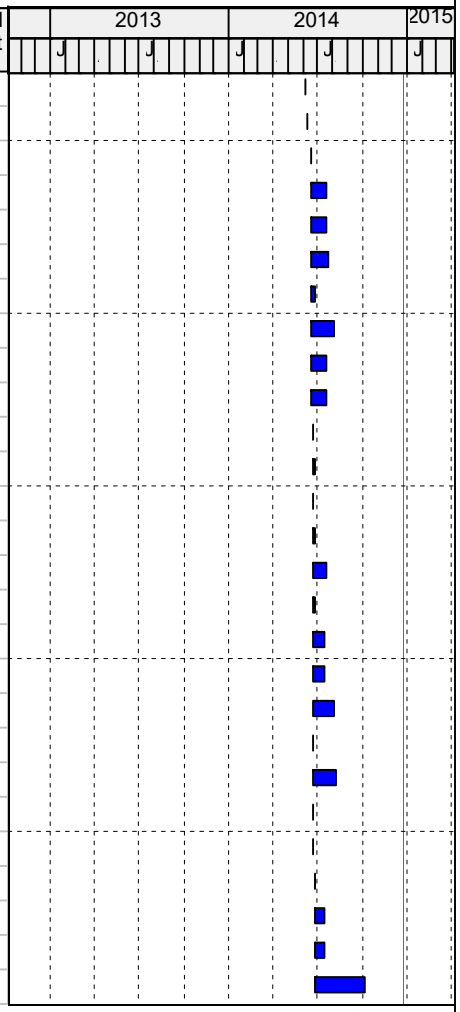


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8604 | L3 Pool - Plumbing R/I | 5 | 0 | 25-Jun-14 A | 10-Nov-14 A | |
| L04-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 26-Jun-14 A | 03-Jul-14 A | |
| L09-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 26-Jun-14 A | 26-Jun-14 A | |
| I-3706 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 26-Jun-14 A | 10-Jul-14 A | |
| L03-8600 | L3 Pool - Framing & HM frames | 5 | 0 | 26-Jun-14 A | 20-Nov-14 A | |
| L05-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L08-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L04-7018 | Electrical Rough-In | 1 | 0 | 27-Jun-14 A | 22-Jul-14 A | |
| L04-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 27-Jun-14 A | 23-Jul-14 A | |
| L03-7020 | HVAC Rough-In | 1 | 0 | 29-Jun-14 A | 15-Jul-14 A | |
| L1RR-8100 | Insulation [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8100 | Insulation [DELETED - included in Ballroom activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8100 | Insulation [DELETED - included in Meeting Rooms ac | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8102 | GWB Hang [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8215 | GWB Tape [DELETED - included in Meeting Rooms a | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8104 | Prime Paint [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8102 | GWB Hang [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8215 | GWB Tape [DELETED - included in Ballroom activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8104 | Prime Paint [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |

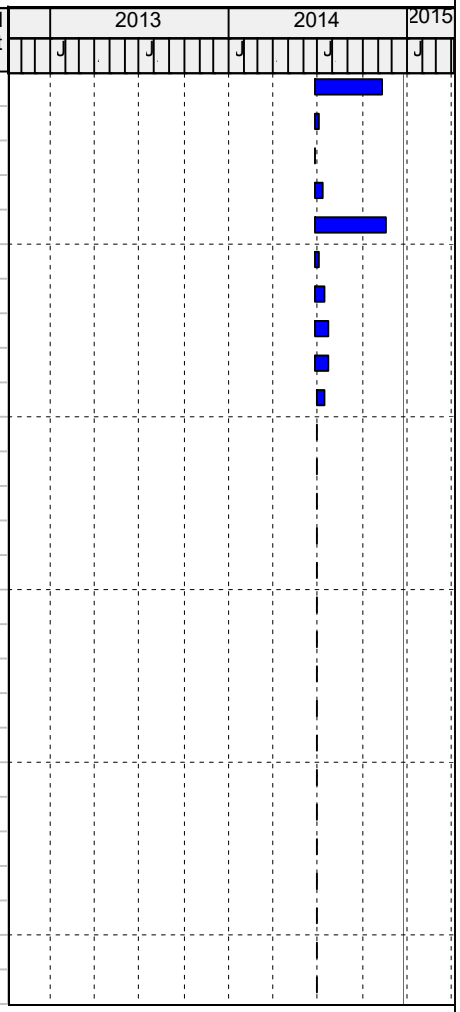



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1RR-8102 | GWB Hang [DELETED - included in Kitchen activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8215 | GWB Tape [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8104 | Prime Paint [DELETED - included in Kitchen activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L03-7018 | Electrical Rough-In | 1 | 0 | 01-Jul-14 A | 14-Jul-14 A | |
| L03-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Jul-14 A | 15-Jul-14 A | |
| L10-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7102 | Install Vertical Heat Pump | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L03-7116 | Frame Walls | 1 | 0 | 02-Jul-14 A | 14-Jul-14 A | |
| L03-7118 | Install HM Door Frame | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L04-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L05-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L07-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L08-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L09-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L10-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L12-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| I-3708 | Complete wall framing at Stair/Elevator 5 (LL3) | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |

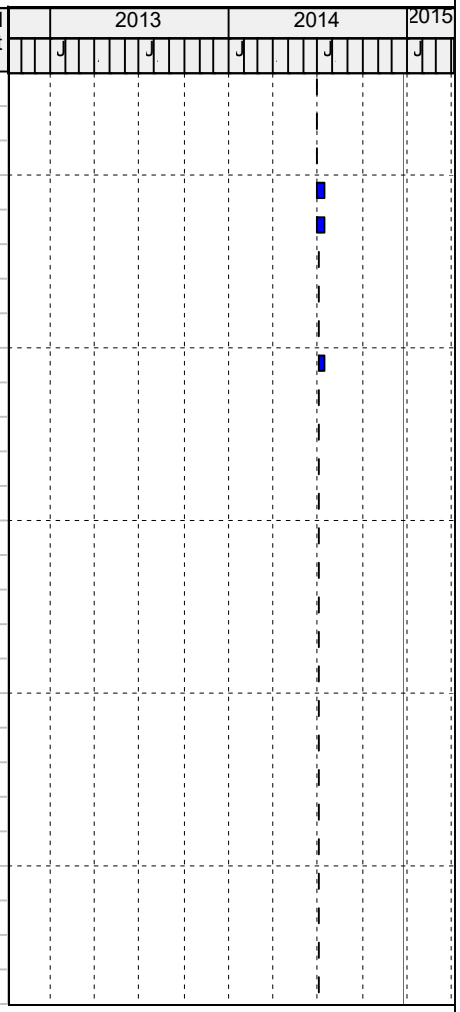



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L11-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 03-Jul-14 A | 07-Jul-14 A | |
| L04-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L05-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L06-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L07-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L08-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L17-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L10-6040 | Test Heat Pumps - L7, L8, L9 and L10 | 3 | 0 | 07-Jul-14 A | 09-Jul-14 A | |
| L10-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L03-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L04-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L05-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L06-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L07-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L08-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L09-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L10-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L12-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |

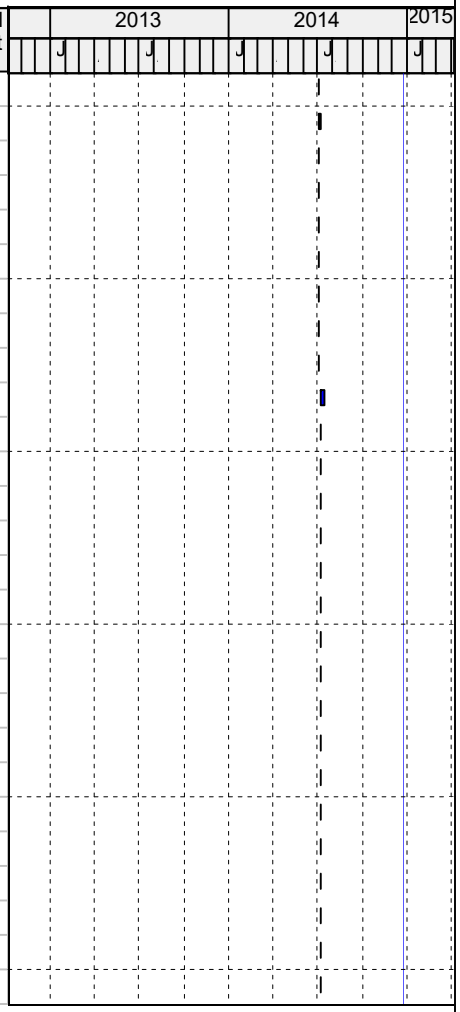



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L11-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Jul-14 A | 29-Jul-14 A | |
| L03-8602 | L3 Pool - Fire Sprinkler R/I | 5 | 0 | 08-Jul-14 A | 22-Jul-14 A | |
| L03-7016 | Install HM door frame | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L11-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L16-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 09-Jul-14 A | |
| L04-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |

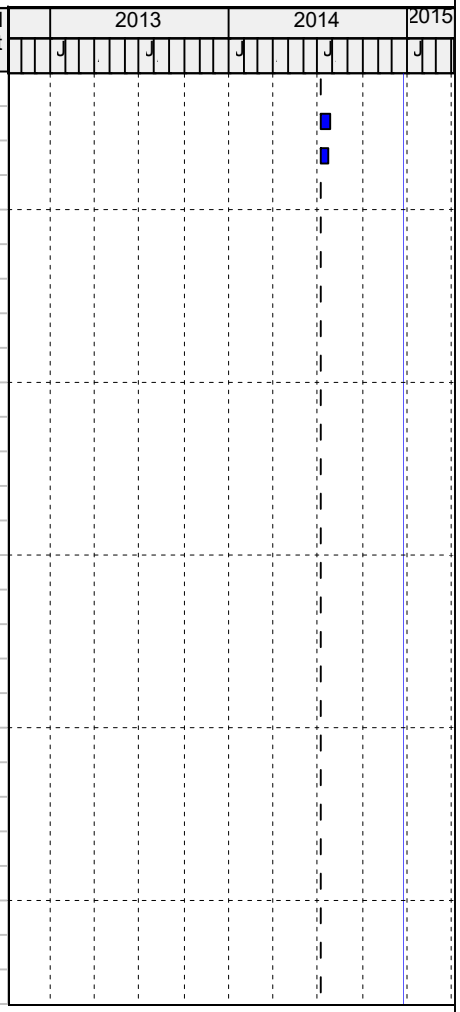



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L12-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| MP-FAB1 | Fabricate and Deliver Bronze Gold Horizontal Panels | 30 | 0 | 09-Jul-14 A | 15-Jul-14 A | |
| L04-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L05-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L06-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L16-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| MP-FAB2 | Fabricate and Deliver Silver Vertical Panels | 45 | 0 | 10-Jul-14 A | 25-Aug-14 A | |
| I-3004 | Issue ASI 38 | 0 | 0 | 11-Jul-14 A | | |
| I-3006 | Release bar area for x-ray examination | 5 | 0 | 11-Jul-14 A | 03-Sep-14 A | |
| L07-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| LL1-Z2-6018a | Complete Mech RI at tower crane opening (LL1) | 4 | 0 | 14-Jul-14 A | 17-Jul-14 A | |
| L08-6223 | Frame Corridor Ceilings | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| SW-2006a | Complete Dry Utilities (Phase 2) | 5 | 0 | 14-Jul-14 A | 24-Jul-14 A | |
| L04-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L04-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L05-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L06-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |

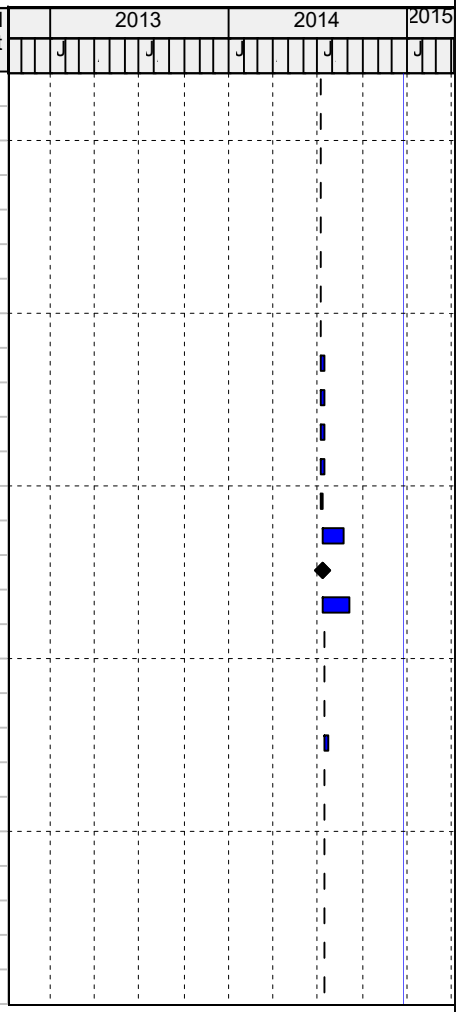



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L04-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L11-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L11-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L12-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L12-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L15-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L15-7102 | Install Vertical Heat Pump | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L1B-6026 | Install operable partition steel | 2 | 0 | 15-Jul-14 A | 08-Aug-14 A | |
| L09-6223 | Frame corridor ceilings | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L03-7120 | Electrical Rough-In | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |

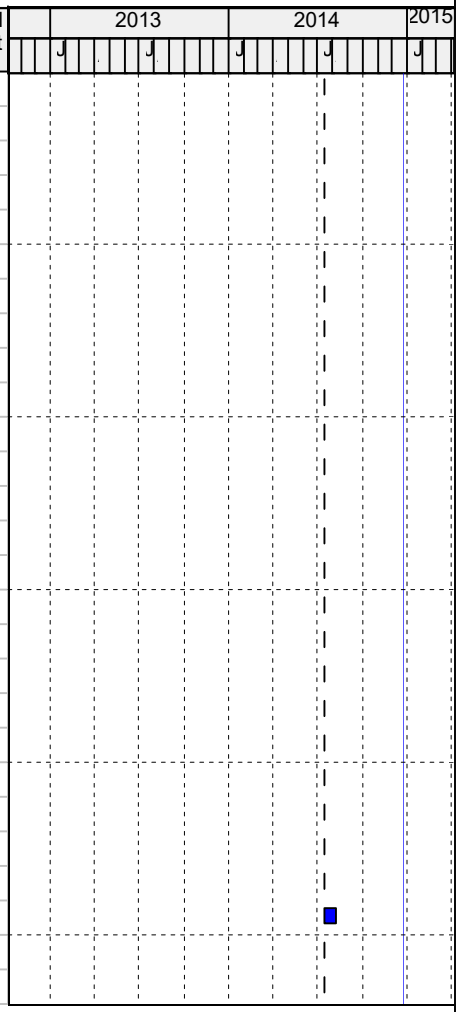



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L07-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L08-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L08-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L09-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L09-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L03-7142 | Install Laundry Chute (All Levels) | 9 | 0 | 15-Jul-14 A | 25-Jul-14 A | |
| LL2-2045 | LL2 - Electrical Room build-out | 15 | 0 | 15-Jul-14 A | 26-Sep-14 A | |
| L03-7122 | HVAC Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L04-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L05-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L06-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L07-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L07-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L08-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L08-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L09-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L09-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |

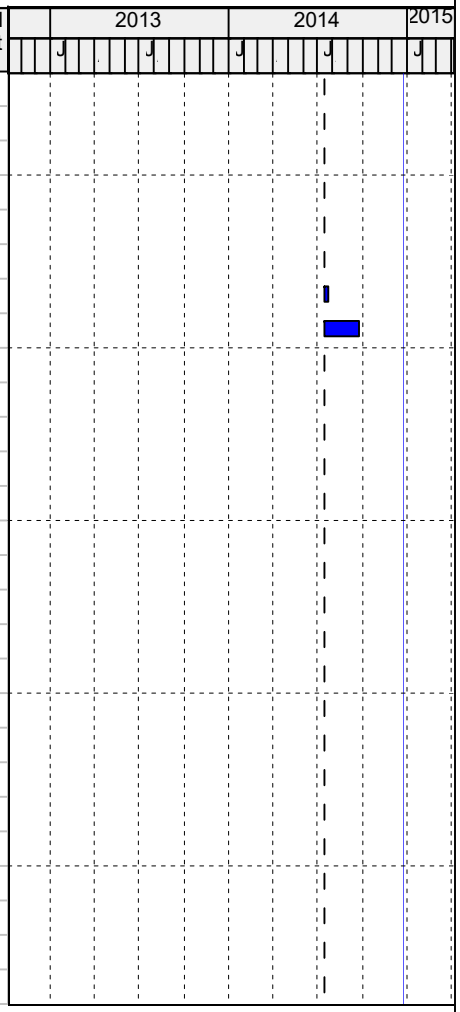



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L11-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L11-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L12-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L12-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L15-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L15-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L16-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L17-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L04-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L04-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L05-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L05-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L06-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L06-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L07-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L08-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L09-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |

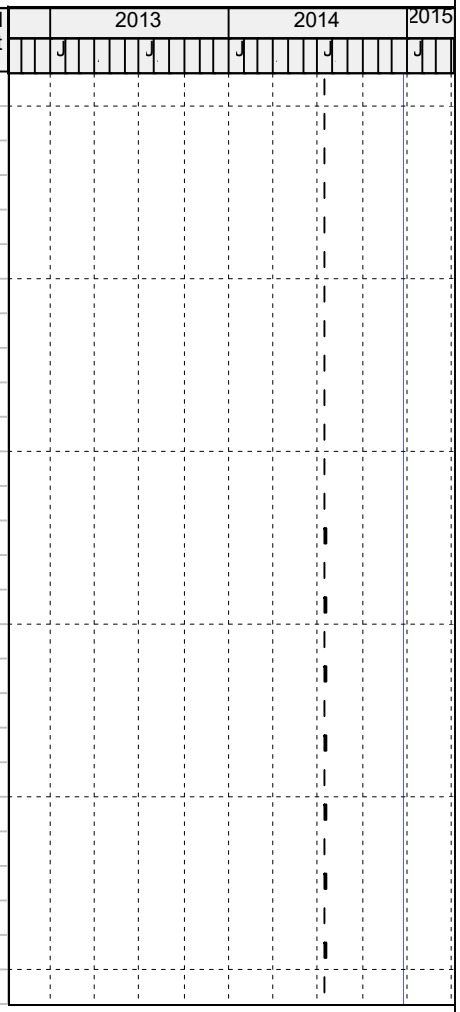



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L11-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L11-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L12-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L12-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L16-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L03-8608 | L3 Pool - Electrical R/I | 5 | 0 | 18-Jul-14 A | 10-Nov-14 A | |
| L03-8610 | L3 Pool - Fire Alarm / Elec Specialties R/I | 5 | 0 | 18-Jul-14 A | 10-Nov-14 A | |
| L15-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L15-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| L17-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L17-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| LL2-2052 | LL2 - Install fuel piping and exhaust duct to Generatc | 8 | 0 | 21-Jul-14 A | 15-Aug-14 A | |
| L04-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L04-7016 | Install HM door frame | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L07-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L08-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L10-7116 | Frame Walls | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L16-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 21-Jul-14 A | 22-Jul-14 A | |
| L16-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |

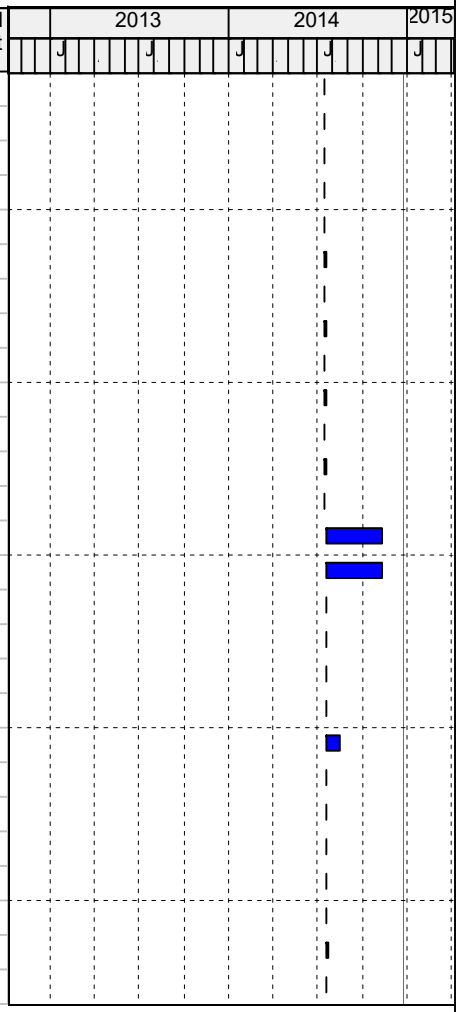



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| MPT-1002 | Tower - Install Elevation 35 (east elevation-south half) | 8 | 0 | 25-Jul-14 A | 04-Aug-14 A | |
| L16-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 25-Jul-14 A | 25-Jul-14 A | |
| L11-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L14-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L15-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L16-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L10-6223 | Frame Corridor Ceilings | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L11-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L15-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L15-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L11-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L14-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L16-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| I-1304 | Prep Kitchen - Additional framing (ASI 30) | 2 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-2302 | Framing "Go Back" work at LL1 for RFI 233 | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| I-2502 | Electrical rework at LL1 for ASIs 7, 9r2, 14, 27 | 4 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| L12-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L1B-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 01-Aug-14 A | 15-Aug-14 A | |
| MPL4-1000 | Upper L4 Ballroom - Install Elevations 1, 2 & 3 (south | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1000 | Tower - Install Elevations 26-27 (west elevation) [DEL | 13 | 0 | 01-Aug-14 A | 01-Aug-14 A | |

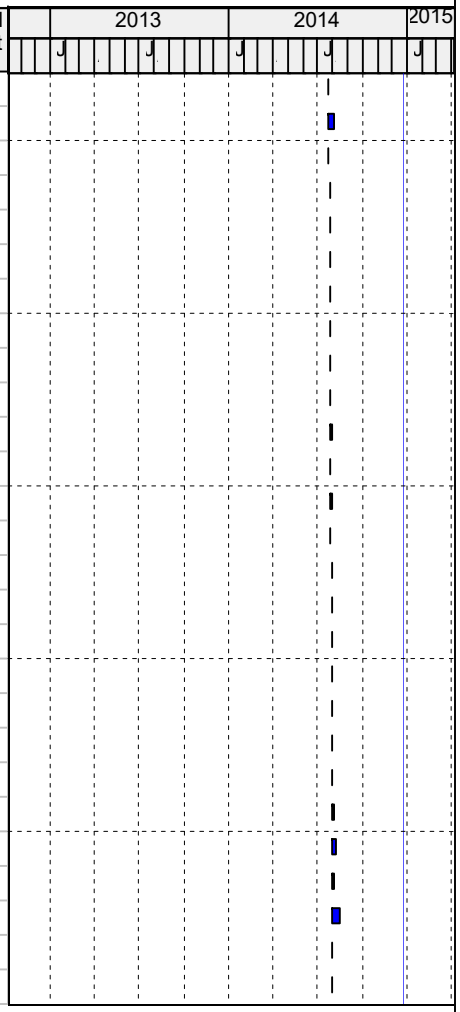



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPP-1002 | Podium - Install Elevations 1 & 2 (west elevation, sou | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPP-1008 | Podium - Install Elevations 7 & 8 (north & east elevati | 9 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1002 | Upper L4 Ballroom - Install Elevation 10 (west elevatic | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1004 | Upper L4 Ballroom - Install Elevation 9 (north elevatio | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1006 | Tower - Install Elevation 40 (east return-east end) [DE | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1010 | Tower - Install Elevations 51 (north elevation) [DELET | 8 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-4004 | East Stitched - Install metal panels [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L11-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L11-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L15-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L14-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L17-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| MPT-1010b | Tower - Install Elevation 45 [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L16-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 04-Aug-14 A | 05-Aug-14 A | |
| L11-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Aug-14 A | 08-Aug-14 A | |
| L04-7020 | HVAC Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |

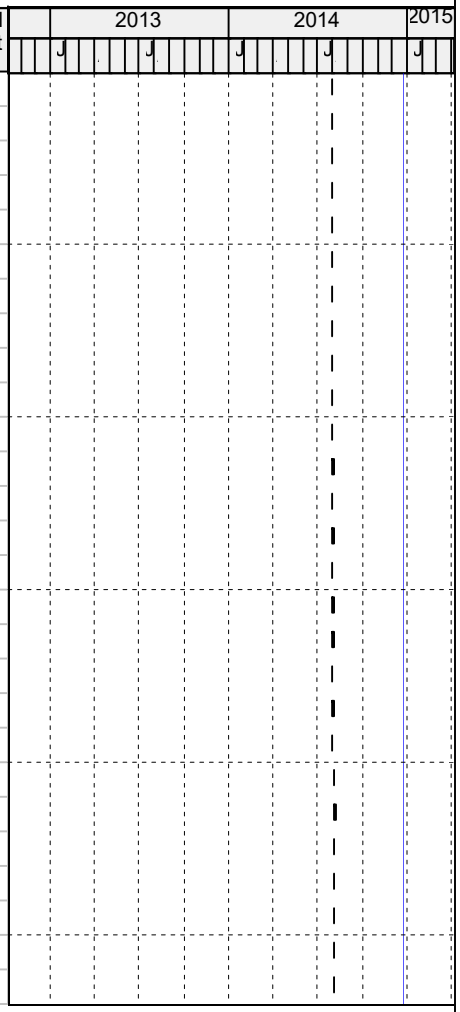



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L14-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L15-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 05-Aug-14 A | 07-Aug-14 A | |
| L05-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L06-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L07-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L08-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L09-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L10-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7018 | Electrical Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L14-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 05-Aug-14 A | 06-Aug-14 A | |
| L14-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| I-4104 | Install added trap primers - LL1 | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L06-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L07-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L08-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L09-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |

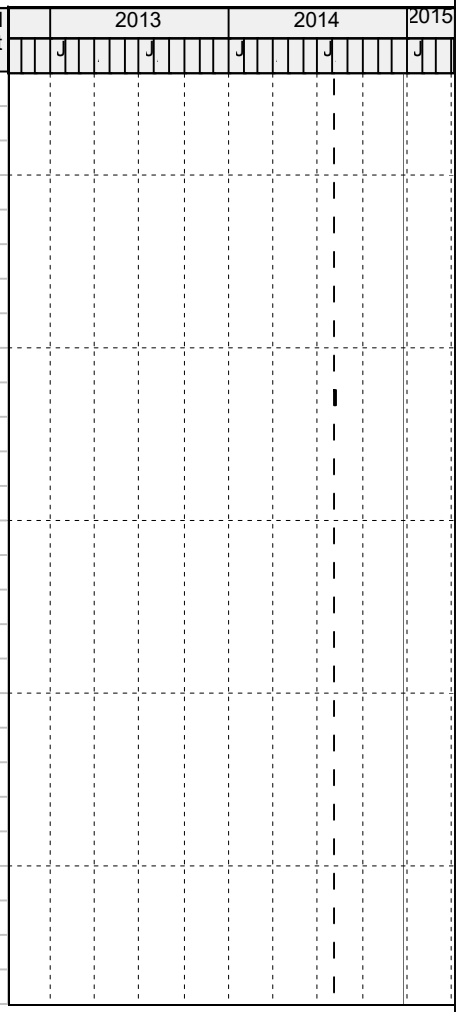



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7020 | HVAC Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L16-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| EL-1220 | Elevator fronts delivered | 0 | 0 | 07-Aug-14 A | | |
| L12-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L12-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-6223 | Frame Corridor Ceilings | 4 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L11-7016 | Install HM door frame | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L12-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L15-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L15-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L16-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L16-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L17-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L17-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-6040 | Test Heat Pumps - L11, L12 and L14 | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| PH-6026 | PH - Insulation/Vapor Barrier/GWB at Exterior Walls | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |

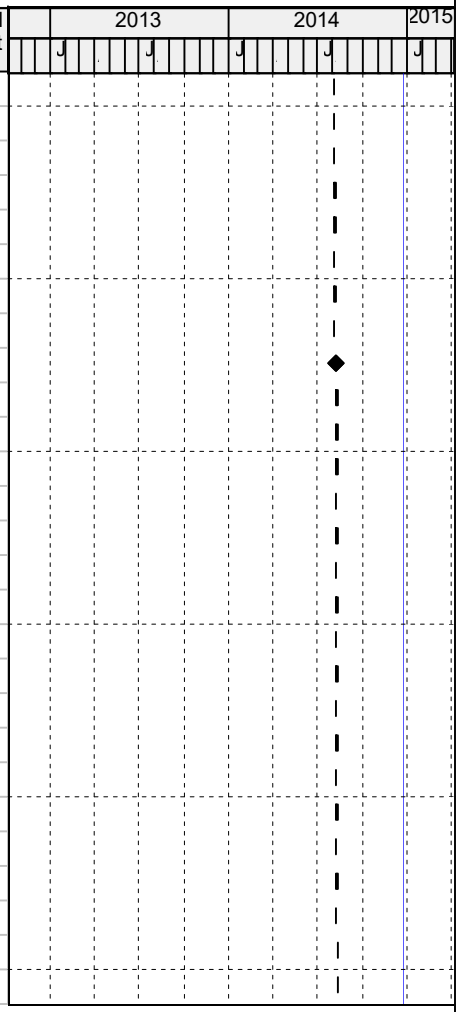



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L11-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-7026 | Inspections for GWB Cover | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 13-Aug-14 A | 13-Aug-14 A | |
| L15-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 14-Aug-14 A | 15-Aug-14 A | |
| LL2E-8108 | LL2 - Set fire pumps and equipment | 5 | 0 | 14-Aug-14 A | 29-Sep-14 A | |
| L10-7028 | GWB Hang/Tape/Finish | 5 | 0 | 14-Aug-14 A | 05-Dec-14 A | |
| L12-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L12-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L16-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L1BOH2-6008 | Int Wall Framing & Inspection | 5 | 0 | 14-Aug-14 A | 20-Aug-14 A | |
| I-4106 | Install added trap primers - L1 | 1 | 0 | 15-Aug-14 A | 15-Aug-14 A | |
| L14-6223 | Frame Corridor Ceilings | 4 | 0 | 15-Aug-14 A | 16-Aug-14 A | |
| L03-8136 | Install Counter Subtops | 3 | 0 | 15-Aug-14 A | 18-Aug-14 A | |
| LL2-2054 | LL2 - GWB, Hang 1st Layer at Laundry Room | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| LL2E-8112 | LL2 - Form/Pour Fire Pump Pads/Curbs | 2 | 0 | 16-Aug-14 A | 18-Aug-14 A | |
| LL1-6014Ia | L1 bar redesign - rework plumbing at ceilings | 10 | 5 | 18-Aug-14 A | 30-Dec-14 | 7 |

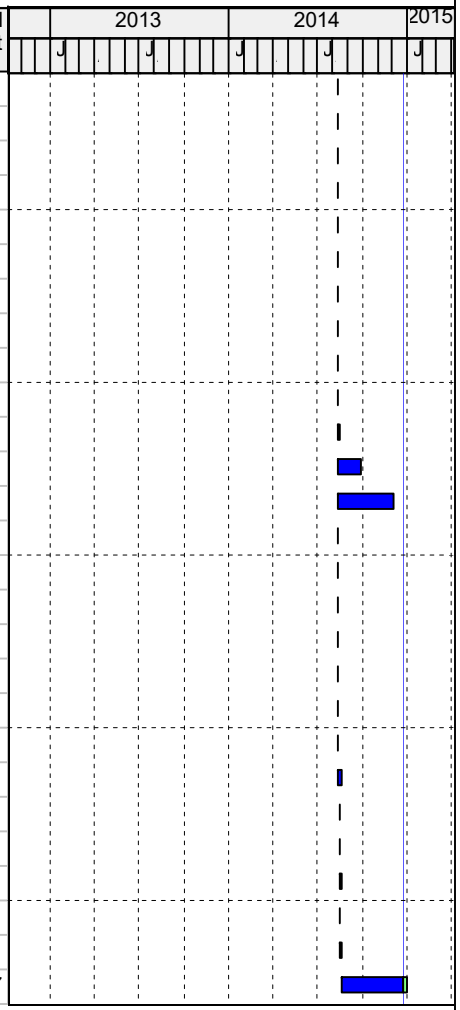



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6223 | Frame Corridor Ceilings | 4 | 0 | 18-Aug-14 A | 21-Aug-14 A | |
| L17-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Aug-14 A | 18-Aug-14 A | |
| L04-8136 | Install Counter Subtops | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-6014Ic | L1 bar redesign - rework electrical at ceilings | 10 | 5 | 18-Aug-14 A | 27-Dec-14 | 11 |
| LL2E-8114 | LL2 - Set Tube Steel at Door | 1 | 0 | 19-Aug-14 A | 19-Aug-14 A | |
| L17-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 20-Aug-14 A | 21-Aug-14 A | |
| L17-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 20-Aug-14 A | 20-Aug-14 A | |
| L05-8136 | Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 26-Aug-14 A | |
| L06-8136 | Bathrooms - Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 13-Oct-14 A | |
| L16-6223 | Frame Corridor Ceilings | 4 | 0 | 21-Aug-14 A | 29-Aug-14 A | |
| L17-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 21-Aug-14 A | 22-Aug-14 A | |
| L17-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 21-Aug-14 A | 21-Aug-14 A | |
| L1BOH2-6016 | Electrical RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6018 | HVAC RI | 4 | 0 | 21-Aug-14 A | 17-Oct-14 A | |
| L15-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7020 | HVAC Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7022 | Fire Sprinkler Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| LL2E-8116 | LL2 - Set Door Jamb | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L04-7028 | GWB Hang/Tape/Finish | 5 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L05-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L05-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L06-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |

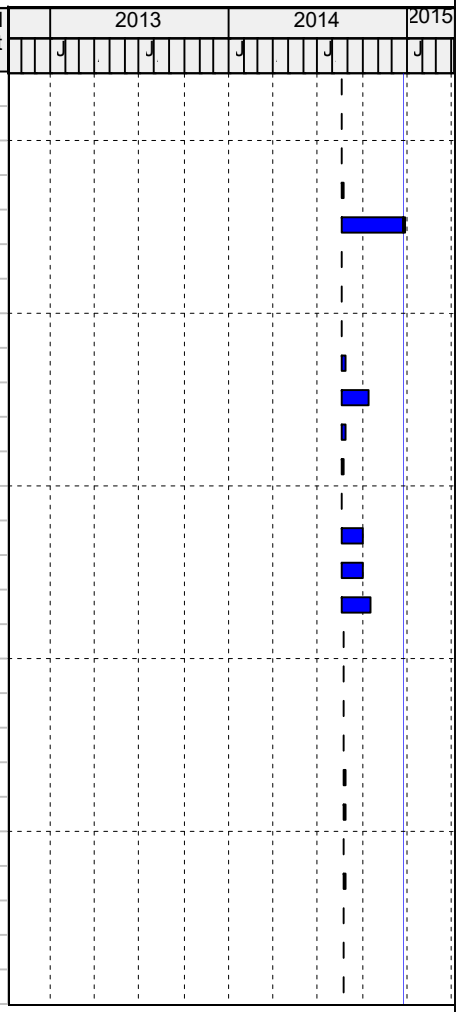



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L03-8123 | Bathroom "Barn Doors" On Site | 0 | 0 | 25-Aug-14 A | | |
| LL3-6026 | LL3 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL2-6026 | LL2 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL1-Z3-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L1BOH2-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |

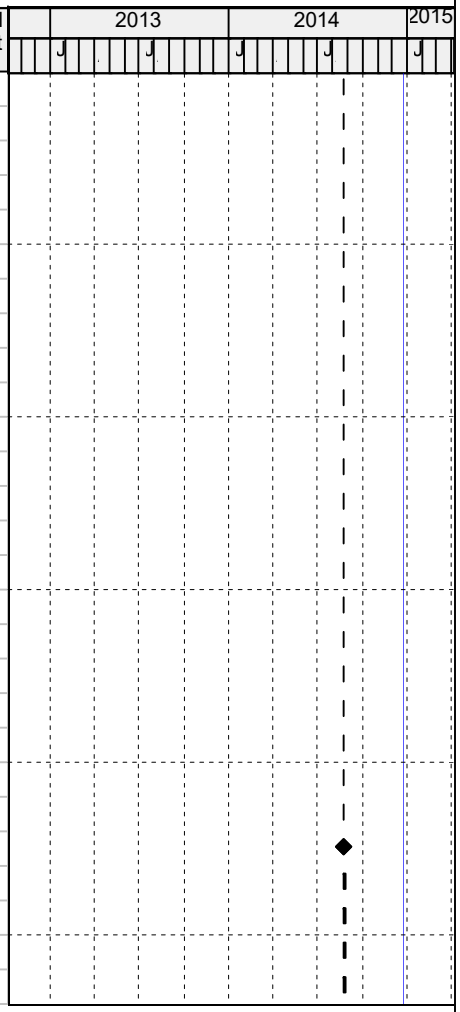



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-6026 | L2 - Set Elevator Fronts (Cars 1-4 | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L03-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L04-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L05-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L06-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L07-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L08-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L09-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L10-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L11-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L12-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L14-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L15-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L16-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L17-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| MPT-1008 | Tower - Install E/W Wing, N. Side West Half (Elev 50,: | 7 | 0 | 26-Aug-14 A | 03-Oct-14 A | |
| L06-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L07-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L08-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L05-7026 | Inspections for GWB Cover | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L05-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L11-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 08-Dec-14 A | |
| L12-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L14-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L03-8105a | Painting - Split Door Jambs | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L09-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L10-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |

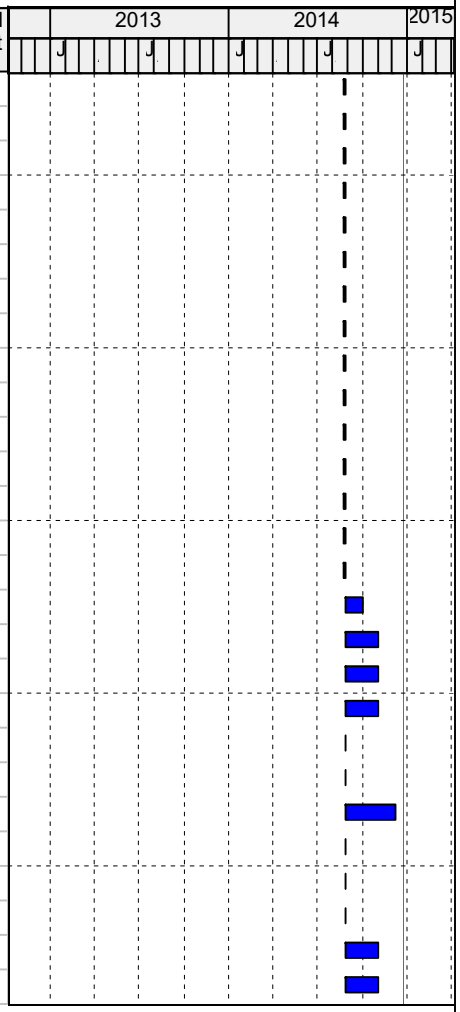


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L12-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L14-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L15-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L16-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L05-8201 | Install ACT Grid @ Corridors | 2 | 0 | 27-Aug-14 A | 28-Aug-14 A | |
| L16-7022 | Fire Sprinkler Rough-In | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L04-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L06-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| EP-5110a | L1 - Install Steel at Revolving Door Opening | 3 | 0 | 27-Aug-14 A | 29-Aug-14 A | |
| L05-8105a | Painting - Split Door Jambs | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| I-4102 | Install added trap primers - LL2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4108 | Install added trap primers - L2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4110 | Install added trap primers - L3 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4112 | Install added trap primers - Roof PH | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| L03-8124d | Flooring On Site and Acclimated | 2 | 0 | 29-Aug-14 A | 01-Sep-14 A | |
| L02-5102 | L2 - Storefront Frames | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| L04-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L05-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L17-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L03-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L12-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L14-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L07-8136 | Install Counter Subtops | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| LL1-Z3-FCC10 | FCC - Set Jamb | 1 | 0 | 02-Sep-14 A | 03-Sep-14 A | |
| MPT-1004 | Tower - Install E/W Wing, S. Side w/o Windows (Elev | 10 | 0 | 03-Sep-14 A | 17-Oct-14 A | |
| L03-7028 | GWB Hang/Tape/Finish | 5 | 0 | 03-Sep-14 A | 02-Dec-14 A | |

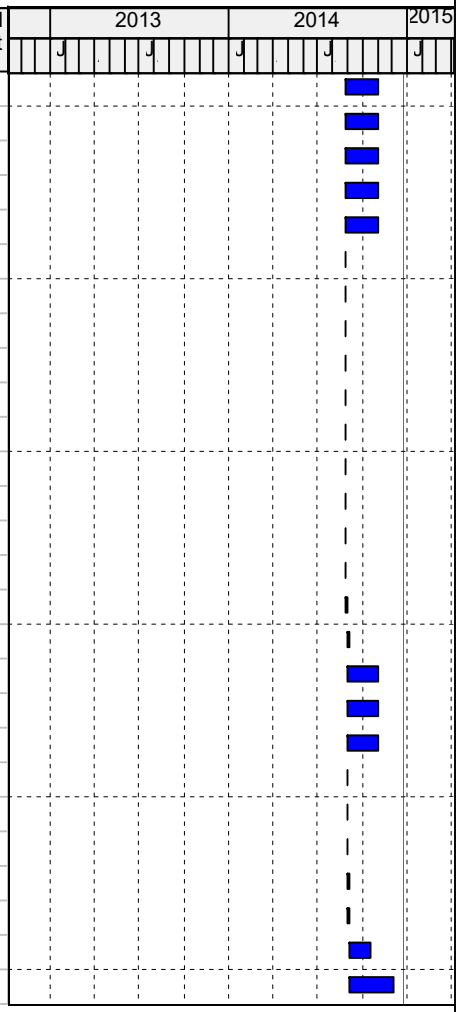



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7028 | GWB Hang/Tape/Finish | 5 | 0 | 03-Sep-14 A | 08-Dec-14 A | |
| L03-8126a | Doors & Hardware On Site | 0 | 0 | 03-Sep-14 A | | |
| LL1-Z3-FCC12 | FCC - Sheetrock Outside Wall | 1 | 0 | 03-Sep-14 A | 03-Sep-14 A | |
| L16-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| L17-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Sep-14 A | 11-Sep-14 A | |
| L02-5104b | L2 - Install Storefront Temporary Enclosures | 1 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| LL1-Z3-FCC14 | FCC - Verify Fire Caulk OK & Inspect Room OK to 2n | 1 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| I-3008 | Coordinate and perform x-ray examination | 7 | 0 | 04-Sep-14 A | 12-Sep-14 A | |
| L02-5104a | L2 - Measure/Fabricate Storefront Glazing | 15 | 0 | 05-Sep-14 A | 18-Sep-14 A | |
| LL1-Z3-FCC16 | FCC - GWB, Hang 2nd Layer | 2 | 0 | 05-Sep-14 A | 08-Sep-14 A | |
| L03-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L15-7018 | Electrical Rough-In | 1 | 0 | 08-Sep-14 A | 08-Sep-14 A | |
| EL-1228 | Construct/Approve elevator lobby framing mockup (L | 3 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| LL2E-8118 | LL2 - Frame Infill, Install Densglass & Inspect at Fire I | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L06-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L08-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L15-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7018 | Electrical Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L3-5104a | L3 - Measure/Fabricate Storefront Glazing | 15 | 0 | 09-Sep-14 A | 30-Sep-14 A | |
| L03-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 23-Sep-14 A | |
| L03-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L04-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L06-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| L08-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |

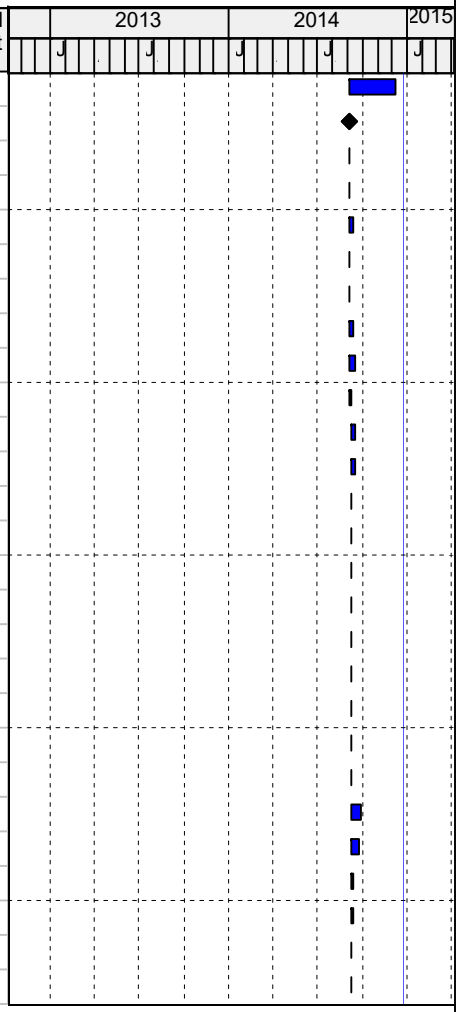



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L06-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L06-7028 | GWB Hang/Tape/Finish | 5 | 0 | 10-Sep-14 A | 02-Dec-14 A | |
| L08-7028 | GWB Hang/Tape/Finish | 5 | 0 | 10-Sep-14 A | 05-Dec-14 A | |
| L15-7026 | Inspections for GWB Cover | 1 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| LL2E-8120 | LL2 - Insulation, Vapor Barrier & Inspect at Fire Pump | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L08-8395 | Framing at Elevator Lobby | 4 | 0 | 11-Sep-14 A | 17-Sep-14 A | |
| L15-7028 | GWB Hang/Tape/Finish | 5 | 0 | 11-Sep-14 A | 08-Dec-14 A | |
| L08-8136 | Install Counter Subtops | 3 | 0 | 11-Sep-14 A | 16-Sep-14 A | |
| L02-6025 | L2 - Framing Go-Back Work (left out for mechanical e | 4 | 0 | 11-Sep-14 A | 02-Oct-14 A | |
| L1-5104a | L1 - Measure/Fabricate Storefront Glazing | 15 | 0 | 12-Sep-14 A | 18-Sep-14 A | |
| L1B-8102c | Finish framing and MEP at Main Ballroom East Wall ( | 10 | 0 | 12-Sep-14 A | 02-Oct-14 A | |
| L09-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L10-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L11-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L12-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L16-7026 | Inspections for GWB Cover | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| MPT-1014 | Tower - Install E/W Wing, N. Side, E. Half (Elev 46-49 | 8 | 0 | 15-Sep-14 A | 28-Oct-14 A | |
| LL2-6032 | LL2 - Complete Framing (Including Elevator Lobby) | 4 | 0 | 15-Sep-14 A | 18-Sep-14 A | |
| L1-5104b | L1 - Install Storefront Temporary Enclosures | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| LL1-Z3-FCC18 | FCC - Install Temp Door | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| LL2-2058a | LL2 - GWB Hang 1st Layer | 5 | 0 | 15-Sep-14 A | 19-Sep-14 A | |
| LL2-2064 | LL2 - Generator Room - Finish Exhaust Piping | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| I-3010 | Prepare proposal for MEP relocations | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| L16-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L07-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |

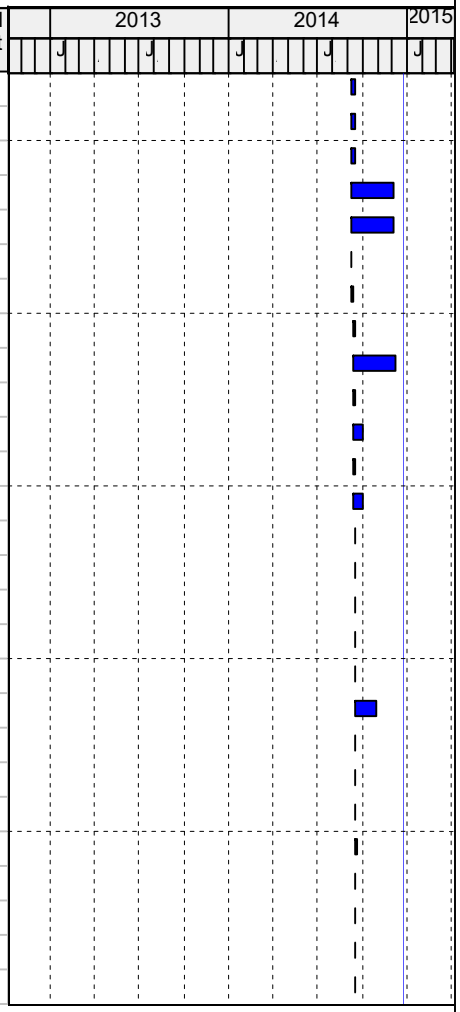



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L10-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L14-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L15-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L03-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| L16-7028 | GWB Hang/Tape/Finish | 5 | 0 | 16-Sep-14 A | 08-Dec-14 A | |
| L17-7018 | Electrical Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L09-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L10-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| LL3-6028 | LL3 - Frame Elevator Lobby | 2 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| LL4-6026 | LL4 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| I-3012 | Owner approve proposal for MEP relocations | 3 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| L11-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L12-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L14-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L15-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L04-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L17-7026 | Inspections for GWB Cover | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L17-7116 | Frame Walls | 4 | 0 | 17-Sep-14 A | 29-Sep-14 A | |
| LL2-2066 | LL2 - Generator Room - Finish Fuel Piping | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L16-8395 | Framing at Elevator Lobby | 4 | 0 | 18-Sep-14 A | 26-Sep-14 A | |
| L02-5104 | L2 - Storefront Glazing | 2 | 0 | 18-Sep-14 A | 22-Sep-14 A | |
| L17-7028 | GWB Hang/Tape/Finish | 5 | 0 | 18-Sep-14 A | 08-Dec-14 A | |
| LL4-6028 | LL4 - Frame Elevator Lobby | 2 | 0 | 18-Sep-14 A | 02-Oct-14 A | |
| MPT-1010a | Tower - Install E/W Wing, West End (Elev 52,53) | 8 | 0 | 18-Sep-14 A | 10-Oct-14 A | |
| LL2-2068 | LL2 - Generator Room - Electrical Finishes | 3 | 0 | 19-Sep-14 A | 30-Sep-14 A | |

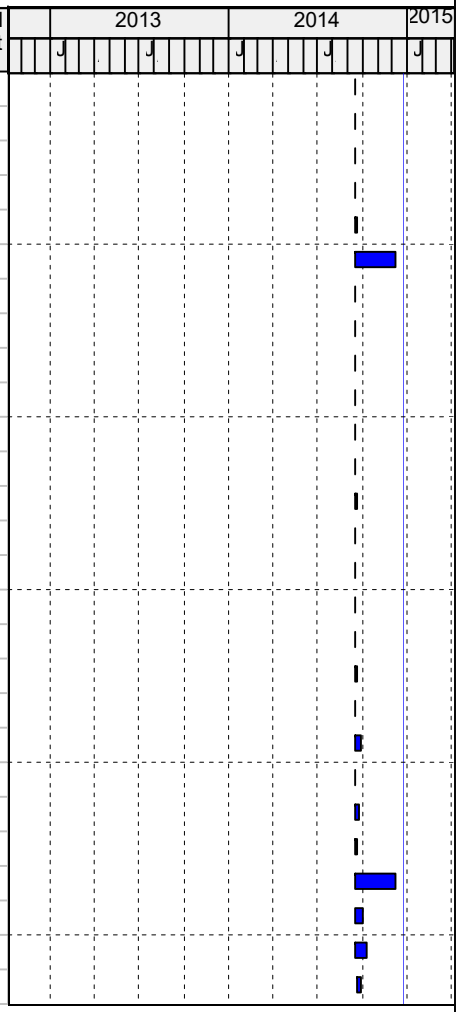



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L09-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L04-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L05-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L03-8140 | Countertops On Site | 0 | 0 | 22-Sep-14 A | | |
| L03-8129a | Shower Doors On Site | 0 | 0 | 22-Sep-14 A | | |
| LL1-Z3-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L1BOH2-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2-2048a | LL2 - Move in Laundry Room Ironer | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2E-8122 | LL2 - Hang GWB at Fire Pump Room | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-FCC20 | FCC - Rough-In and Install Panels | 25 | 0 | 22-Sep-14 A | 21-Nov-14 A | |
| I-3014 | Core drill for MEP relocations | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L05-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L07-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 05-Dec-14 A | |
| L09-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 05-Dec-14 A | |
| L14-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 08-Dec-14 A | |
| L04-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L05-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L06-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L07-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L04-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L06-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L04-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |

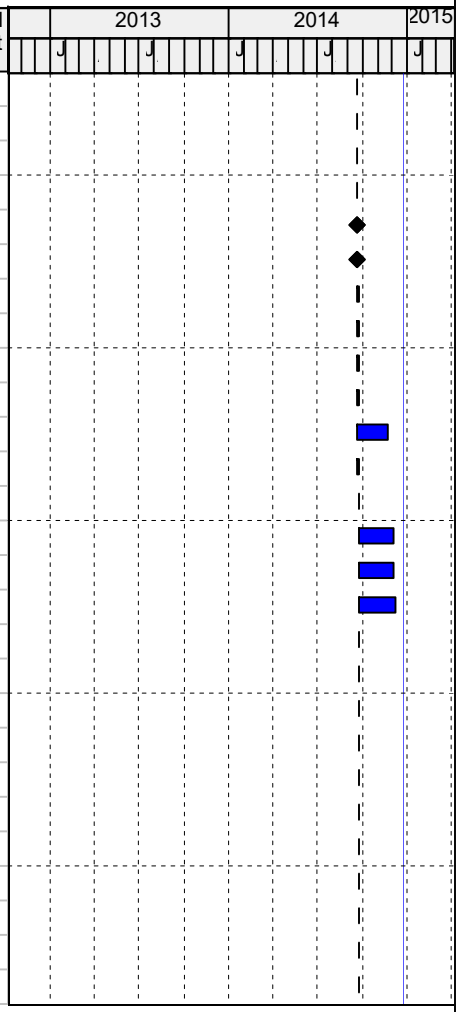



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-7122 | HVAC Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| LL2-2058 | LL2 - Tape/Finish Laundry Room | 3 | 0 | 24-Sep-14 A | 26-Sep-14 A | |
| L08-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L17-8395 | Framing at Elevator Lobby | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L05-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L06-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L07-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L08-7120 | Electrical Rough-In | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| LL2E-8124 | LL2 - Temp-In Louver Opening at Fire Pump Room | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L1-5104c | L1 - Install Storefront at Main Entry Facade | 5 | 0 | 25-Sep-14 A | 10-Oct-14 A | |
| L16-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L08-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L10-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L16-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L17-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L17-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L09-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L11-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |

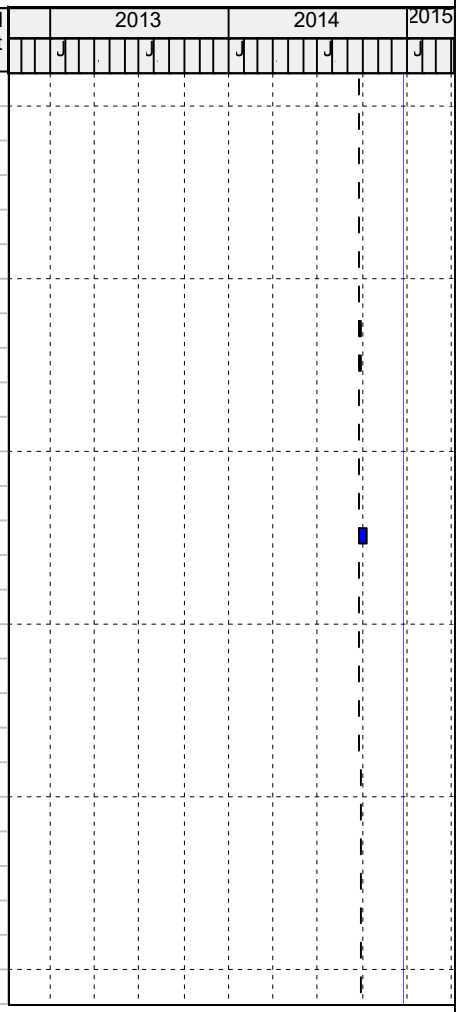



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L14-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L15-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L17-7118 | Install HM Door Frame | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| LL3-6030 | LL3 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL4-6030 | LL4 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL2-6034 | LL2 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L1BOH2-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L02-6030 | L2 - Framing at Elevator Lobby & North Half | 4 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| MPT-1022 | Tower - Caulking, west | 8 | 0 | 29-Sep-14 A | 03-Nov-14 A | |
| PH-6015 | PH - Set Boilers and Pumps | 12 | 0 | 29-Sep-14 A | 15-Oct-14 A | |
| L11-8204 | Bathrooms - Vinyl Wall Coverings | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L10-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L17-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L11-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L12-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L07-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 30-Sep-14 A | 08-Oct-14 A | |
| L11-8201 | Install ACT Grid @ Corridors | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L09-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L09-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L11-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L12-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L14-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L15-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| LL2-2072 | Generator - Complete generator and annunciator cor | 5 | 0 | 30-Sep-14 A | 21-Oct-14 A | |

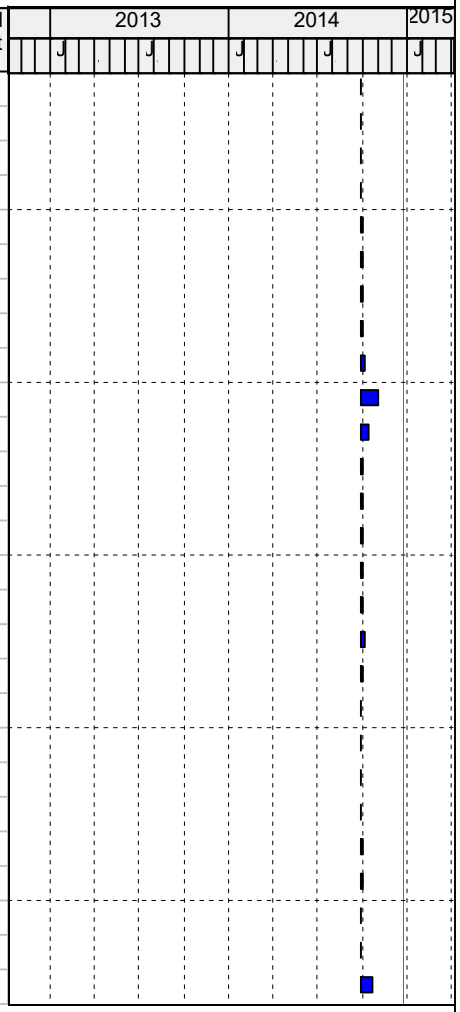



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6040 | Test Heat Pumps - L16 and L17 | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L17-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L14-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L03-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |

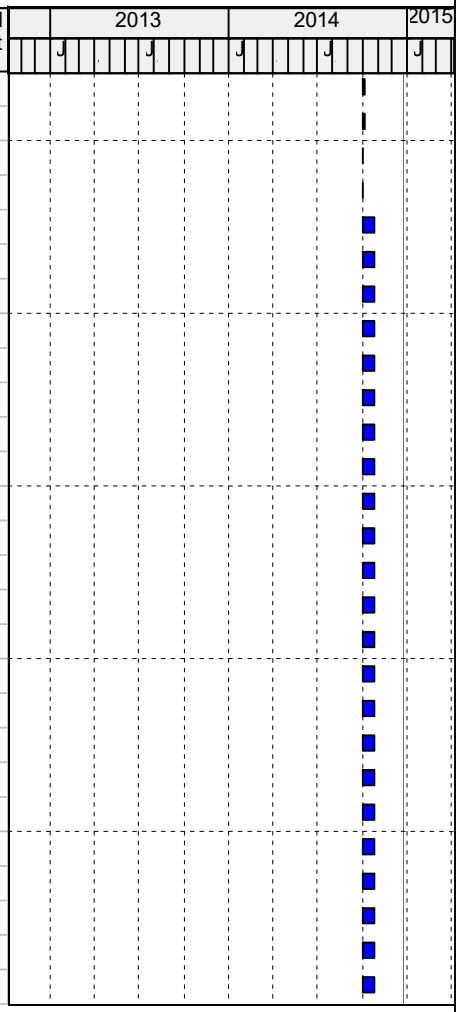



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L11-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L12-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L12-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L14-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L16-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L17-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L09-8136 | Install Counter Subtops | 3 | 0 | 01-Oct-14 A | 03-Oct-14 A | |
| L02-6032 | L2 - Electrical RI at Elevator Lobby & North Half | 5 | 0 | 01-Oct-14 A | 08-Oct-14 A | |
| SW-2306 | Prep, grind and overlay at 11th Ave, 3rd Place & 2nd | 5 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 01-Oct-14 A | 16-Dec-14 A | |
| L16-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |

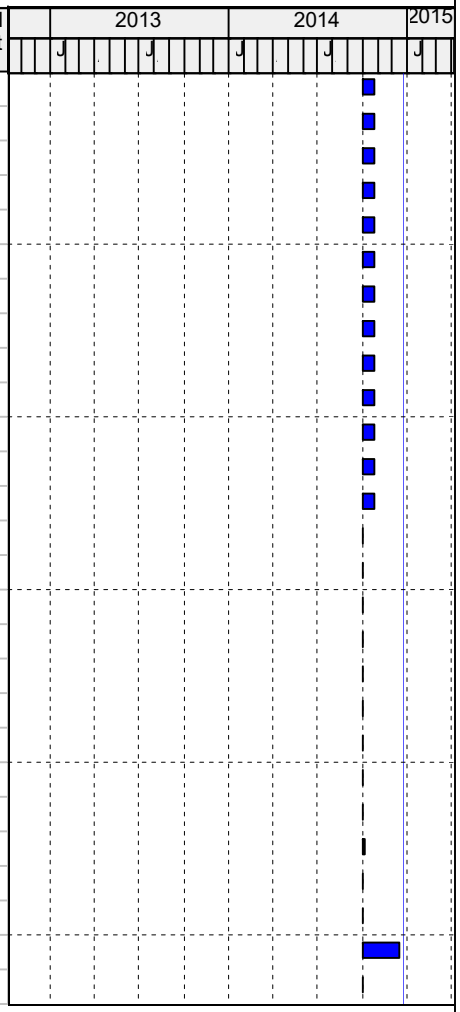



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L14-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L15-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1BOH2-8130 | Inspections For Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L02-6024a | L2 - Inspections - South Half | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L06-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| L17-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| LL2-2074 | Generator - Install fuel fill | 2 | 0 | 03-Oct-14 A | 06-Oct-14 A | |
| L07-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| MPT-1020 | Tower - Install E/W Wing, East End (Elev 41,44) | 5 | 0 | 06-Oct-14 A | 18-Oct-14 A | |
| LL1-8102a | GWB Hang/Tape (Ceilings) | 10 | 0 | 06-Oct-14 A | 18-Nov-14 A | |
| L1BOH2C-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6014 | Complete Plumbing RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6016 | Complete Electrical RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6018 | Complete HVAC RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L03-8200a | New murals on site (date estimated) | 0 | 0 | 06-Oct-14 A | | |
| SW-2100 | Zone 1 - Survey curb & site lighting | 2 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 06-Oct-14 A | 06-Oct-14 A | |
| L1BOH2-8100 | Insulation | 4 | 0 | 07-Oct-14 A | 13-Oct-14 A | |
| L17-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L12-8201 | Install ACT Grid @ Corridors | 2 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| L10-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 07-Oct-14 A | 20-Oct-14 A | |
| LL1-Z3-6032 | GWB Hang/Tape at Elevator Lobby | 5 | 2 | 07-Oct-14 A | 23-Dec-14 | 17 |

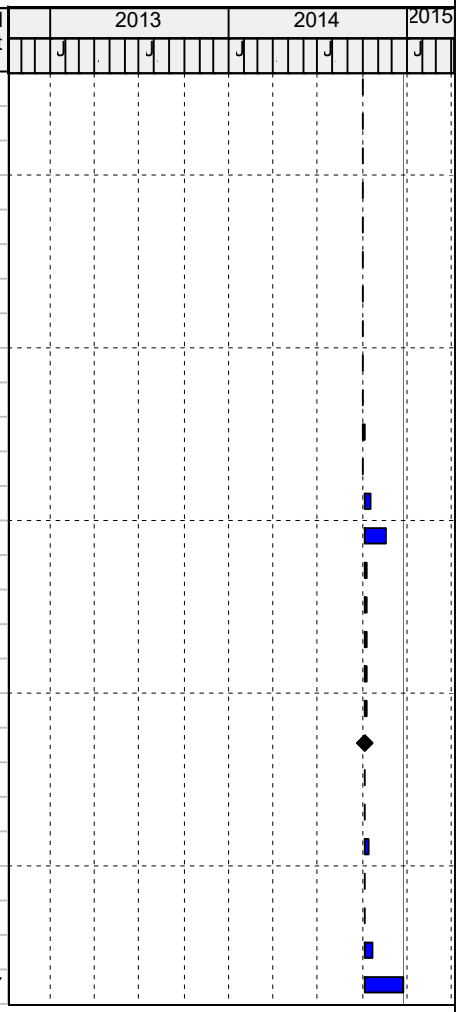


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8216x | Vinyl Wall Coverings - Install Murals | 2 | 1 | 07-Oct-14 A | 22-Dec-14 | 27 |
| L1B-8102b | GWB Hang (Walls) & Inspection - Exterior Wall at Cor | 3 | 0 | 07-Oct-14 A | 09-Oct-14 A | |
| RF-4048 | Tower Roof - Install davit arms | 3 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| LL2-2076 | Generator - Install fuel fill mechanical piping | 4 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L12-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L09-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L03-8633 | Pool - Install waterproofing & test | 3 | 0 | 08-Oct-14 A | 17-Oct-14 A | |
| L03-8130 | Install Door Hardware | 3 | 0 | 08-Oct-14 A | 28-Oct-14 A | |
| L10-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L02-8102a | L2 - GWB Hang / Tape / Finish - South Half | 7 | 0 | 09-Oct-14 A | 27-Oct-14 A | |
| SW-2102 | Zone 1 - Vacate SE corner | 2 | 0 | 09-Oct-14 A | 11-Oct-14 A | |
| SW-2106 | Zone 1 - Sawcut and remove asphalt | 4 | 0 | 09-Oct-14 A | 14-Oct-14 A | |
| L11-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 09-Oct-14 A | |
| SW-2200 | Zone 2 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |
| SW-2300 | Zone 3 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |
| SW-2108 | Zone 1 - Install east footing drain | 4 | 0 | 10-Oct-14 A | 20-Oct-14 A | |
| L04-8130 | Install Door Hardware | 3 | 0 | 10-Oct-14 A | 29-Oct-14 A | |
| ML-5962 | Man/Material Lifts - Remove Roof Lift Stop | 0 | 0 | | 11-Oct-14 A | |
| I-1102 | Additional work at new L17 guest rooms | 5 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| LL2-2046 | LL2 - Generator Room - Misc. Finishes | 3 | 0 | 13-Oct-14 A | 21-Nov-14 A | |
| RF-4008 | Tower Roof - Install corrugated metal panels | 5 | 0 | 13-Oct-14 A | 03-Nov-14 A | |
| MPT-1018b | Tower - Roof cornice frame & sheath | 6 | 0 | 13-Oct-14 A | 24-Oct-14 A | |
| L02-8100a | L2 - Insulation - South Half | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| SW-2112 | Zone 1 - Grade for curb and gutter | 3 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| SW-2202 | Zone 2 - Install site lighting | 5 | 0 | 13-Oct-14 A | 24-Nov-14 A | |
| SW-2204 | Zone 2 - Repave utility trenches | 4 | 0 | 13-Oct-14 A | 22-Oct-14 A | |
| L12-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 13-Oct-14 A | |

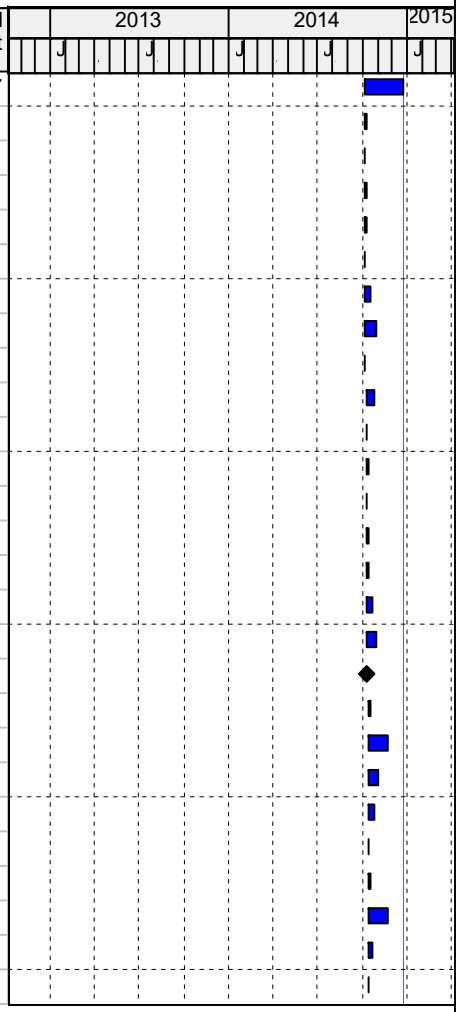



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2302 | Zone 3 - Grade for curb and gutter | 2 | 0 | 14-Oct-14 A | 01-Dec-14 A | |
| L14-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 14-Oct-14 A | 16-Oct-14 A | |
| L05-8130 | Install Door Hardware | 3 | 0 | 14-Oct-14 A | 03-Nov-14 A | |
| L14-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 14-Oct-14 A | |
| L16-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L15-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 15-Oct-14 A | 17-Oct-14 A | |
| L15-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 15-Oct-14 A | |
| SW-2206 | Zone 2 - Grade for curb and gutter | 2 | 0 | 16-Oct-14 A | 20-Oct-14 A | |
| MPP-1000 | Podium - Install W/S/N Elevations (Elev 1-5, 6,9-19,2 | 10 | 0 | 20-Oct-14 A | 10-Dec-14 A | |
| L06-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 20-Oct-14 A | 23-Oct-14 A | |
| LL2-8106a | LL2 - Pinned Insulation | 4 | 1 | 20-Oct-14 A | 22-Dec-14 | 37 |
| L1B-8102d | GWB Hang (Walls) & Inspection - Main Ballroom East | 1 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| SW-2114 | Zone 1 - FRP curb and gutter | 2 | 0 | 20-Oct-14 A | 14-Nov-14 A | |
| RF-4044 | Ballroom Roof - Install metal coping | 3 | 0 | 20-Oct-14 A | 13-Nov-14 A | |
| L08-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 21-Oct-14 A | 23-Oct-14 A | |
| MPT-1018 | Tower - Install Roof Penthouse (Elev 36b,37,38.39) | 5 | 0 | 21-Oct-14 A | 05-Dec-14 A | |
| L11-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2208 | Zone 2 - FRP curb and gutter | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2304 | Zone 3 - FRP curb and gutter | 3 | 0 | 21-Oct-14 A | 02-Dec-14 A | |
| L15-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L06-8130 | Install Door Hardware | 3 | 0 | 21-Oct-14 A | 03-Nov-14 A | |
| I-5100 | Resolve changes (ASI's and RFI's) | 1 | 12 | 21-Oct-14 A | 09-Jan-15 | 0 |

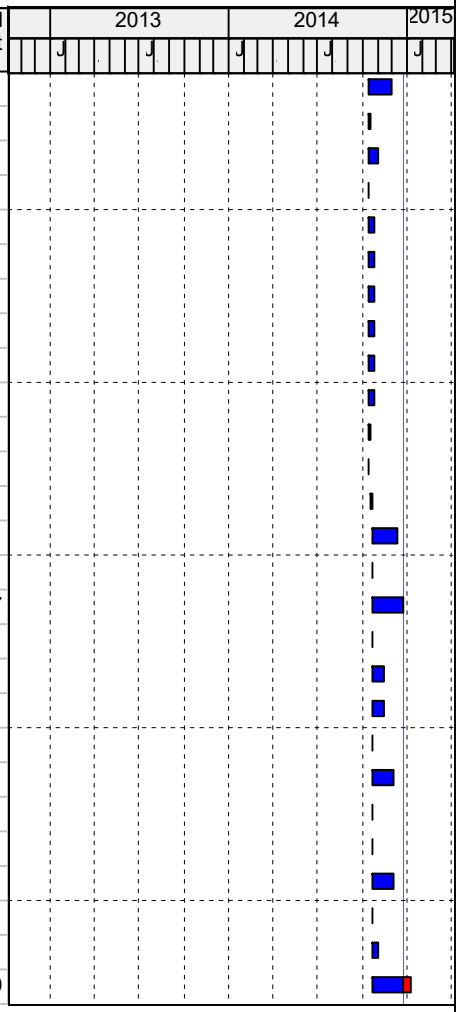



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8634 | Pool - Install reinforcing steel & inspect | 5 | 0 | 22-Oct-14 A | 30-Oct-14 A | |
| MPT-1016 | Tower - Install N/S Wing, S. End W. of Manlift (Elev 2 | 5 | 0 | 22-Oct-14 A | 05-Dec-14 A | |
| SW-2116 | Zone 1 - Fine grade for sidewalk | 3 | 2 | 22-Oct-14 A | 09-Jan-15 | 31 |
| LL4-8106 | LL4 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| LL3-8106 | LL3 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L14-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L08-8130 | Install Door Hardware | 3 | 0 | 22-Oct-14 A | 04-Nov-14 A | |
| L07-8130 | Install Door Hardware | 3 | 0 | 22-Oct-14 A | 03-Nov-14 A | |
| L03-8606 | L3 Pool - HVAC R/I | 3 | 0 | 23-Oct-14 A | 27-Oct-14 A | |
| L09-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 23-Oct-14 A | 03-Nov-14 A | |
| L12-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| LL2-2078 | Generator - Install fuel fill control wiring | 2 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| RF-4050 | Roof at Manlift - Erect steel | 1 | 0 | 24-Oct-14 A | 24-Oct-14 A | |
| CO-7204 | Cx - Gas Service established | 0 | 0 | | 24-Oct-14 A | |
| L1BOH2-8102 | GWB Hang (Walls) | 4 | 0 | 27-Oct-14 A | 07-Nov-14 A | |
| L04-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 27-Oct-14 A | 12-Nov-14 A | |
| RF-4052 | Roof at Manlift - Framing/sheathing/air barrier (inspec | 4 | 0 | 27-Oct-14 A | 30-Oct-14 A | |
| LL2-2080 | Generator - Complete generator accessories (battery) | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| LL2-2082 | Generator - Cx fuel fill | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| L09-8130 | Install Door Hardware | 3 | 0 | 28-Oct-14 A | 04-Nov-14 A | |
| CO-7158 | Generator - Interim electrical inspection | 1 | 0 | 29-Oct-14 A | 29-Oct-14 A | |
| LL2-2070 | LL2 - Generator Room - Generator Ready for Startup | 0 | 0 | | 30-Oct-14 A | |
| LL2-2084 | Generator - Initial fuel fill | 1 | 0 | 30-Oct-14 A | 30-Oct-14 A | |
| CO-7200 | Cx - Penthouse Mechanical Installation Complete | 0 | 0 | | 30-Oct-14 A | |
| EL-6028 | Elev 6 - RFI-761: Response, pricing, complete work (r | 20 | 5 | 30-Oct-14 A | 30-Dec-14 | 32 |
| L03-8636 | Pool - Shotcrete | 1 | 0 | 31-Oct-14 A | 31-Oct-14 A | |
| RF-4054 | Roof at Manlift - Final mechanical installations | 4 | 0 | 31-Oct-14 A | 05-Nov-14 A | |

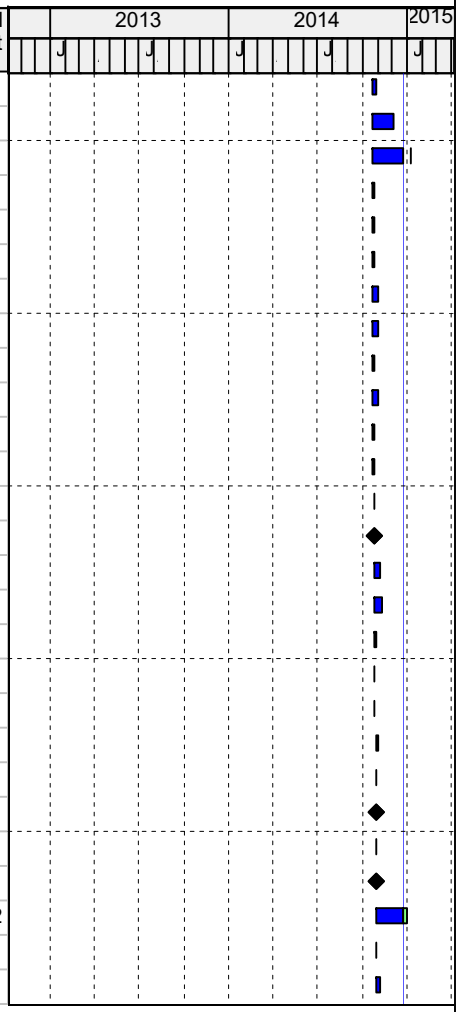



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| RF-4056 | Roof at Manlift - Final electrical connections | 2 | 0 | 31-Oct-14 A | 05-Nov-14 A | |
| CO-7130 | Fire Alarm - Point-To-Point Wiring | 18 | 3 | 01-Nov-14 A | 24-Dec-14 | 23 |
| L03-8404 | GWB Hang/Tape Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 14-Nov-14 A | |
| L04-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 14-Nov-14 A | |
| L05-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 17-Nov-14 A | |
| L06-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 17-Nov-14 A | |
| L03-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L04-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L05-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L06-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L07-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L08-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L09-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L10-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L11-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L12-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L14-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L15-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L16-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L17-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L14-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 03-Nov-14 A | 06-Nov-14 A | |
| MPT-1024 | (A) Caulking - Elevation 41 (east elevation above poo | 7 | 0 | 03-Nov-14 A | 16-Dec-14 A | |
| CO-7206 | Cx - Purge/Prove Gas-Fed Equipment and Feeder Li | 7 | 0 | 03-Nov-14 A | 09-Nov-14 A | |
| L07-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 17-Nov-14 A | |
| L08-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L09-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L10-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |

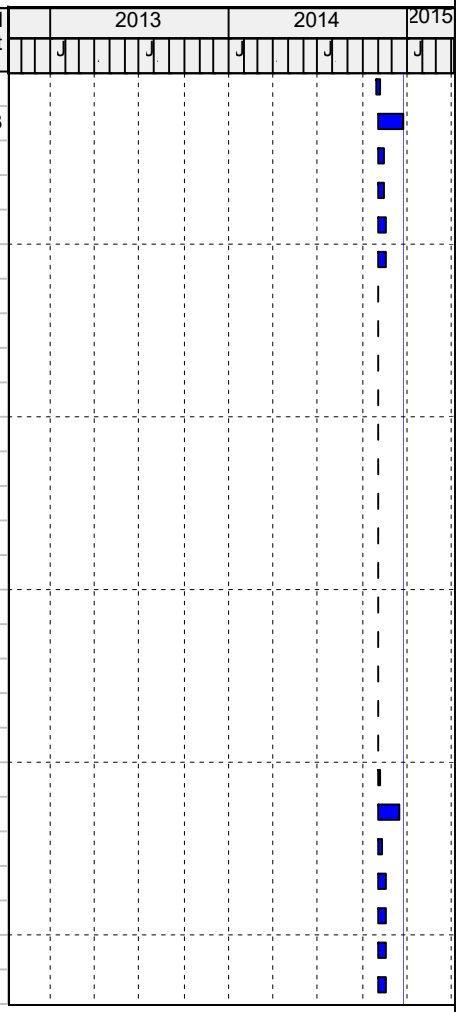



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L11-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 04-Nov-14 A | 15-Dec-14 A | |
| L11-8130 | Install Door Hardware | 3 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L10-8130 | Install Door Hardware | 3 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L11-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 18-Nov-14 A | |
| L12-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 19-Nov-14 A | |
| L14-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 19-Nov-14 A | |
| MPP-1010 | Podium - Install East Elevation (Elev 5 & 7) | 7 | 0 | 05-Nov-14 A | 10-Dec-14 A | |
| CO-7162 | Generator - Load bank testing | 1 | 0 | 05-Nov-14 A | 05-Nov-14 A | |
| CO-7202 | Cx - Electrical Internal Bus & LL2-L17 Bus Duct Energ | 0 | 0 | | 05-Nov-14 A | |
| CO-7202a | Cx - Energize normal power distribution | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| L15-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 19-Nov-14 A | |
| L16-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 20-Nov-14 A | |
| L17-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 20-Nov-14 A | |
| RF-4058 | Roof at Manlift - Install roofing | 2 | 0 | 06-Nov-14 A | 07-Nov-14 A | |
| CO-7164 | Generator - Final electrical inspection | 1 | 0 | 06-Nov-14 A | 06-Nov-14 A | |
| L15-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 07-Nov-14 A | 12-Nov-14 A | |
| L03-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L03-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L04-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L04-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L05-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L05-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L06-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L06-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L07-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L07-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |

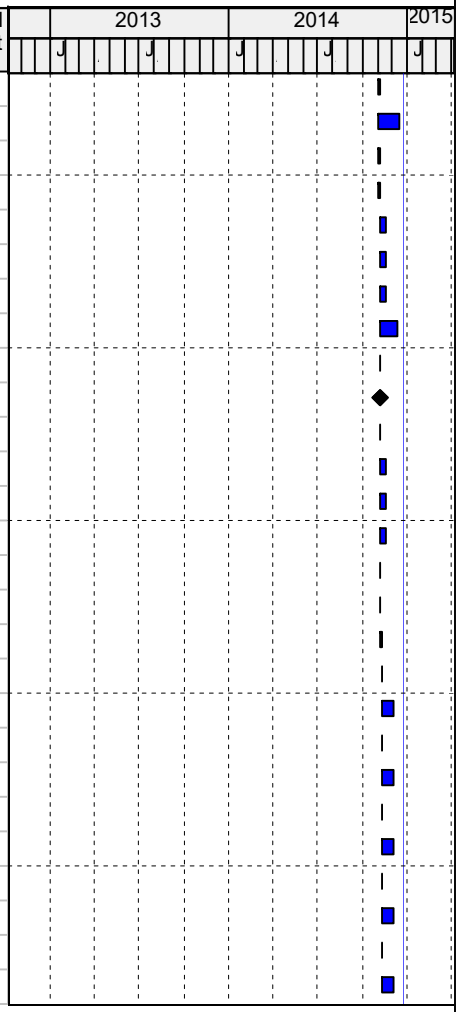



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L08-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L09-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L09-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L10-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L10-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L11-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L11-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L12-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L12-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L14-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L14-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L15-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L15-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L16-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L16-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L17-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L17-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L05-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| L06-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 10-Nov-14 A | 11-Nov-14 A | |
| MPT-1032 | Tower - Install sign backing NW (Elev 51,52) | 4 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L12-8130 | Install Door Hardware | 3 | 0 | 10-Nov-14 A | 12-Nov-14 A | |
| EL-1230 | Elev 1&2 - Complete hoistway ventilation | 13 | 0 | 10-Nov-14 A | 15-Dec-14 A | |
| EL-1232 | Elev 1&2 - Wire & startup AC split units | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-1234 | Elev 1&2 - Install EMR doors, hardware & labeling | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-3428 | Elev 3&4 - Complete hoistway ventilation | 13 | 0 | 10-Nov-14 A | 15-Dec-14 A | |
| EL-3430 | Elev 3&4 - Wire & startup AC split units | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |

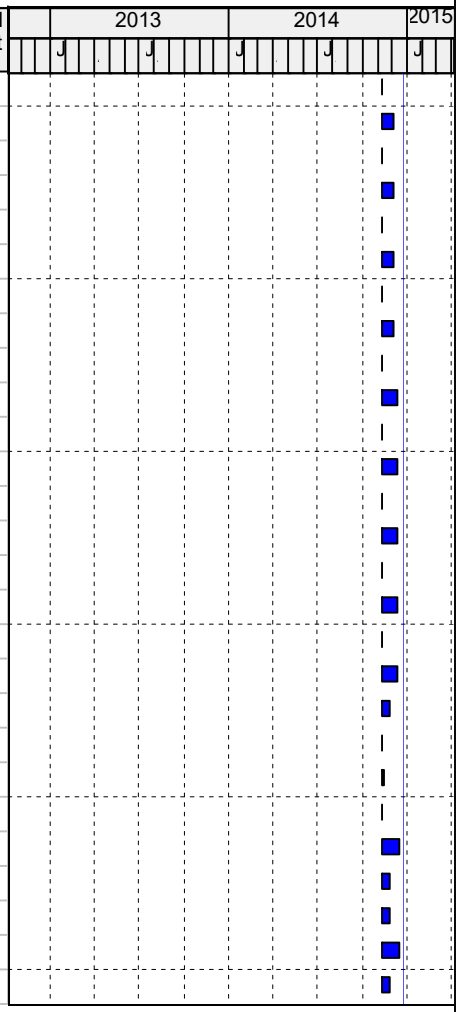



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-3432 | Elev 3&4 - Install EMR doors, hardware & labeling | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-6030 | Elev 6 - Complete fire-rated assemblies at hoistway, l | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| L07-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 11-Nov-14 A | 12-Nov-14 A | |
| L16-8106 | Paint - Accent Walls | 2 | 0 | 11-Nov-14 A | 12-Nov-14 A | |
| L14-8130 | Install Door Hardware | 3 | 0 | 11-Nov-14 A | 13-Nov-14 A | |
| L03-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 12-Nov-14 A | 18-Nov-14 A | |
| SW-2104 | Zone 1 - Install lighting conduit at SE corner | 2 | 0 | 12-Nov-14 A | 14-Nov-14 A | |
| L16-8111 | Paint - Door Jambs | 2 | 0 | 12-Nov-14 A | 13-Nov-14 A | |
| EL-6010i | Elev 6 - Pit Slab Correction (form/pour/strip/clean) | 10 | 0 | 12-Nov-14 A | 26-Nov-14 A | |
| SW-2024 | Zone 4 - FRP Porte Cochere planter & bench | 6 | 0 | 12-Nov-14 A | 04-Dec-14 A | |
| L08-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| SW-2109 | Zone 1 - Install irrigation sleeves | 2 | 0 | 13-Nov-14 A | 14-Nov-14 A | |
| MPT-1026 | (C) Caulking - Elevation 47 (north elevation, east half | 10 | 0 | 13-Nov-14 A | 19-Dec-14 A | |
| L16-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| L15-8130 | Install Door Hardware | 3 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| L04-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 14-Nov-14 A | 19-Nov-14 A | |
| SW-2203 | Zone 2 - Install irrigation sleeves | 2 | 0 | 14-Nov-14 A | 24-Nov-14 A | |
| SW-2316 | Zone 3 - Demolish manlift shack and base | 5 | 0 | 17-Nov-14 A | 20-Nov-14 A | |
| I-1610 | Enclosure at manlift - Install exterior wall panels & ins | 5 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| L04-8140 | Install window sills | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| L03-8140x | Install window sills | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| L16-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| SW-2014 | Porte Cochere - Electrical rough-in | 5 | 0 | 17-Nov-14 A | 08-Dec-14 A | |
| LL1-Z3-FCC24 | FCC - Complete ceiling and access panels (RFI 734) | 13 | 8 | 17-Nov-14 A | 05-Jan-15 | 33 |
| LL1-Z3-FCC26 | FCC - Program FACP | 20 | 12 | 17-Nov-14 A | 09-Jan-15 | 18 |
| L06-8140 | Install window sills | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L05-8140 | Install window sills | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |

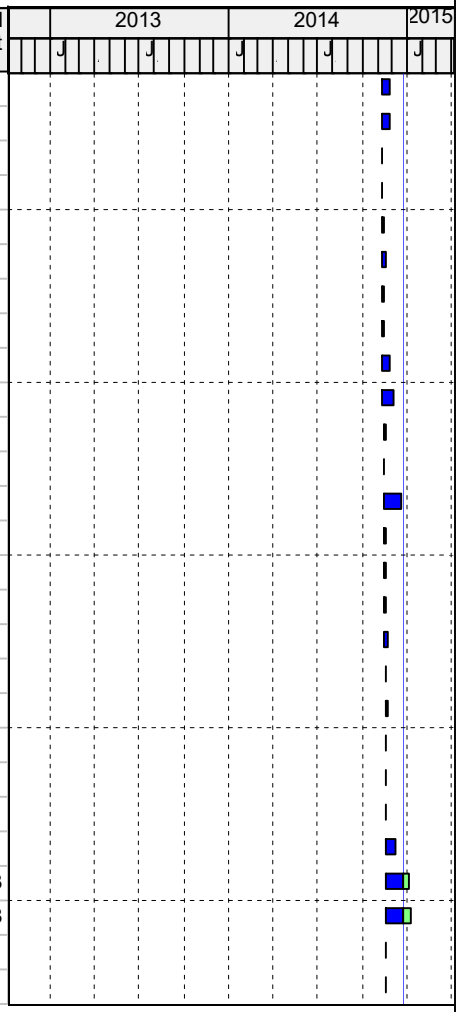



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8129 | Bathrooms - Install Shower Doors | 4 | 1 | 19-Nov-14 A | 22-Dec-14 | 31 |
| L16-8130 | Install Door Hardware | 3 | 0 | 19-Nov-14 A | 02-Dec-14 A | |
| L08-8140 | Install window sills | 2 | 0 | 19-Nov-14 A | 19-Nov-14 A | |
| L07-8140 | Install window sills | 2 | 0 | 19-Nov-14 A | 19-Nov-14 A | |
| I-1616 | Enclosure at manlift - Patch/repair concrete shear wal | 3 | 0 | 19-Nov-14 A | 21-Nov-14 A | |
| L10-8140 | Install window sills | 2 | 0 | 20-Nov-14 A | 20-Nov-14 A | |
| L09-8140 | Install window sills | 2 | 0 | 20-Nov-14 A | 20-Nov-14 A | |
| I-1622 | Manlift finishes - Install windows & caulk | 4 | 0 | 20-Nov-14 A | 03-Dec-14 A | |
| LL2-2060 | LL2 - Paint Laundry Room | 3 | 0 | 21-Nov-14 A | 24-Nov-14 A | |
| L03-8616 | L3 Pool - GWB above ceiling | 2 | 0 | 21-Nov-14 A | 22-Nov-14 A | |
| L1K-8340 | Install walk-in cooler/freezer (BY OTHERS) | 2 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L10-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| L16-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| SW-2110 | Zone 1 - Adjust utilities structures | 5 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| SW-2214 | Zone 2 - Adjust utilities structures | 2 | 0 | 24-Nov-14 A | 25-Nov-14 A | |
| MPT-1030 | Tower - Install sign backing NE (Elev 44) | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| SW-2012 | Porte Cochere - Install cornice[DELETED SEE REV M | 8 | 0 | 24-Nov-14 A | 05-Dec-14 A | |
| L03-8650 | L3 Pool - Build scaffold at pool pit | 2 | 0 | 24-Nov-14 A | 25-Nov-14 A | |
| EL-6032 | Elev 6 - Install pit ladder | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| EL-6034 | Elev 6 - Install pit jack & hoistway pistons; connect hy | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| L06-8129 | Bathrooms - Install Shower Doors | 4 | 1 | 25-Nov-14 A | 22-Dec-14 | 29 |
| L02-8104a | L2 - Int Painting - South Half | 2 | 0 | 25-Nov-14 A | 26-Nov-14 A | |
| SW-2016 | Porte Cochere - Complete framing | 3 | 0 | 25-Nov-14 A | 01-Dec-14 A | |
| LL2-2096 | LL2 - Install FRP at Laundry Room | 8 | 0 | 25-Nov-14 A | 05-Dec-14 A | |
| I-1602 | Enclosure at manlift - Install shear wall clips and inspe | 4 | 0 | 26-Nov-14 A | 05-Dec-14 A | |
| L07-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| SW-2318 | Zone 3 - Install catch basin | 1 | 0 | 26-Nov-14 A | 26-Nov-14 A | |

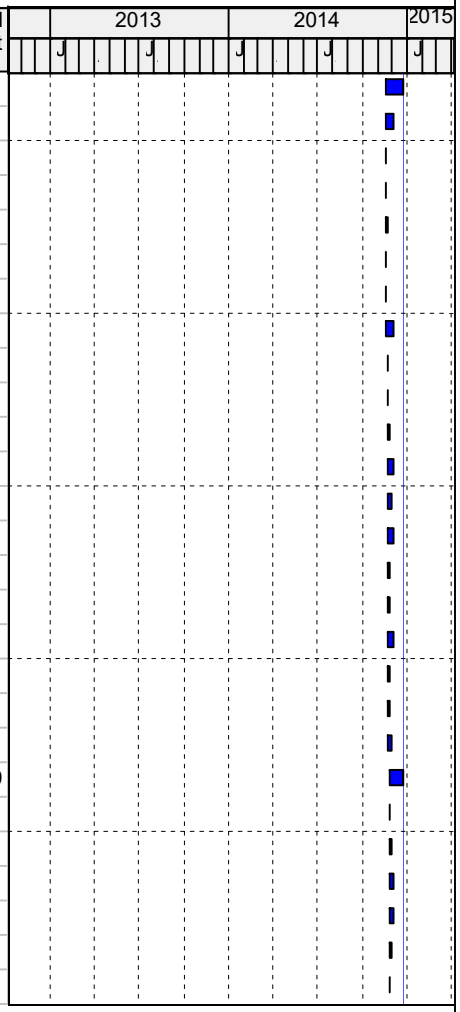



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8652 | L3 Pool - Frame ceiling | 4 | 0 | 26-Nov-14 A | 04-Dec-14 A | |
| L08-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 01-Dec-14 A | 04-Dec-14 A | |
| L02-6016a | L2 - Electrical Room Buildout | 5 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| SW-2210 | Zone 2 - Fine grade for sidewalk | 5 | 2 | 01-Dec-14 A | 07-Jan-15 | 30 |
| SW-2310 | Zone 3 - Install irrigation sleeves | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| RF-4040 | L2.5 Horseshoe - Install sheet metal capping[DELETI | 3 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| MPT-1042 | Enclosure at manlift - air barrier & inspect | 5 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| CO-7208 | Cx - Start-Up Pumps | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| CO-7210 | Cx - Start-Up VFD's | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| L17-8106 | Paint - Accent Walls | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| I-1630 | Manlift finishes - Framing, corridor ceilings & inspect | 4 | 0 | 01-Dec-14 A | 09-Dec-14 A | |
| EL-6036 | Elev 6 - Install shunt trip breaker | 5 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| L17-8111 | Paint - Door Jambs | 2 | 0 | 02-Dec-14 A | 03-Dec-14 A | |
| SW-2018 | Porte Cochere - GWB hang/tape | 3 | 1 | 02-Dec-14 A | 22-Dec-14 | 34 |
| L03-8654 | L3 Pool - HVAC drops at ceiling & inspect | 3 | 0 | 02-Dec-14 A | 05-Dec-14 A | |
| L11-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 03-Dec-14 A | 08-Dec-14 A | |
| SW-2308 | Zone 3 - Install site lighting | 5 | 0 | 03-Dec-14 A | 04-Dec-14 A | |
| L10-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 03-Dec-14 A | 15-Dec-14 A | |
| I-1632 | Manlift finishes - Electrical rough-in & inspect | 2 | 0 | 03-Dec-14 A | 10-Dec-14 A | |
| SW-2028 | Zone 4 - Scan Porte Cochere deck | 2 | 0 | 04-Dec-14 A | 05-Dec-14 A | |
| I-1624 | Manlift finishes - Install batt insulation & inspect | 2 | 0 | 04-Dec-14 A | 04-Dec-14 A | |
| I-1626 | Manlift finishes - Shim window openings | 2 | 0 | 04-Dec-14 A | 05-Dec-14 A | |
| I-1628 | Manlift finishes - Install vapor barrier & inspect | 2 | 0 | 04-Dec-14 A | 08-Dec-14 A | |
| I-1608 | Tower - Install N/S Wing, S. End at manlift (Elev 32) [I | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1012 | Tower - Install N/S Wing, S. End E. Side Concrete (El | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| PC-4012 | Porte Cochere - Install sheet metal capping[DELETEI | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4046 | Tower Roof - Install sheet metal capping[DELETED S | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |

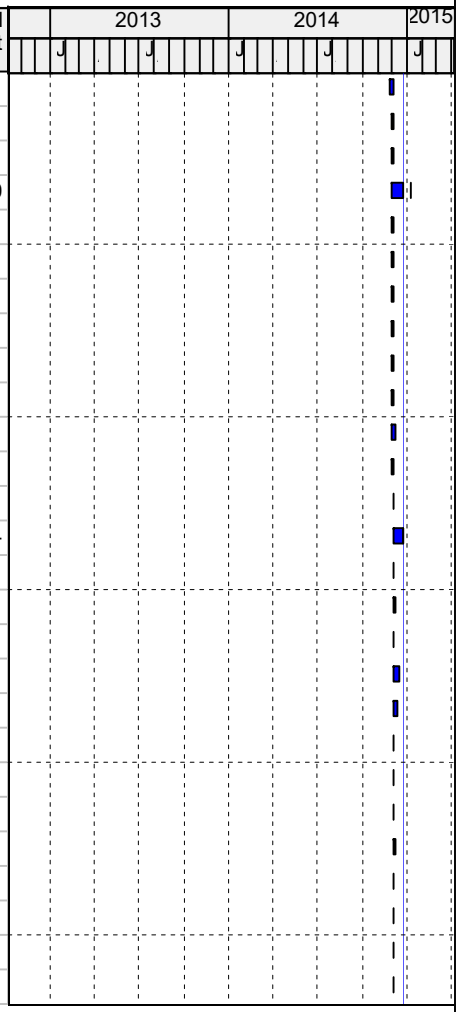



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| RF-4060 | Roof at Manlift - Install corrugated metal panels[DELE | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4062 | Roof at Manlift - Install sheet metal capping[DELETE | 2 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4064 | Pool Green Roof - Install sheet metal capping[DELET | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1040 | Tower - Install N/S Wing, S, End (Elev 30)[DELETED | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1044 | Enclosure at manlift - Install sign backing south[DELE | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1612 | Enclosure at manlift - Caulking[DELETED SEE REV M | 8 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1614 | Enclosure at manlift - Install rigid insulation at shear w | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1618 | Enclosure at manlift - Install framing at shear wall[DEI | 5 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1620 | Enclosure at manlift - Install hat channel over framing | 5 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| L03-8656 | L3 Pool - Electrical rough-in at ceiling & inspect | 3 | 0 | 05-Dec-14 A | 19-Dec-14 A | |
| L1K-8344 | Set kitchen hoods | 8 | 0 | 06-Dec-14 A | 15-Dec-14 A | |
| L12-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L03-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |
| L04-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |
| L05-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |
| SW-2312 | Zone 3 - Fine grade for sidewalk | 1 | 1 | 08-Dec-14 A | 05-Jan-15 | 30 |
| RF-4042 | Pool Roof - Install metal coping at high roof | 2 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L17-8130 | Install Door Hardware | 3 | 0 | 08-Dec-14 A | 11-Dec-14 A | |
| L09-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L03-8658 | L3 Pool - Fire sprinkler drops at ceiling & inspect | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L04-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L05-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L07-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L08-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |

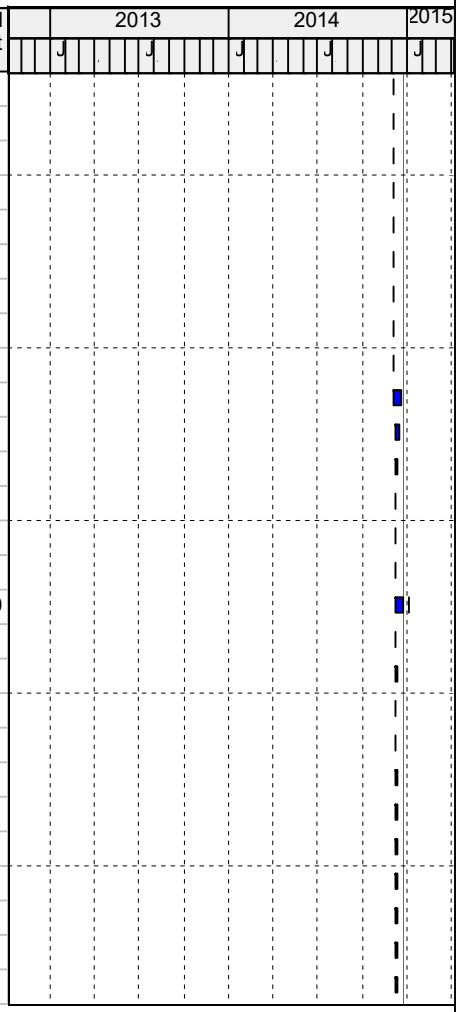



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L14-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L15-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 09-Dec-14 A | 12-Dec-14 A | |
| L03-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L07-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L08-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L04-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L05-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L07-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L08-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| RF-4072 | Pool Roof - Install metal coping | 3 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L17-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 09-Dec-14 A | 12-Dec-14 A | |
| L07-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 1 | 09-Dec-14 A | 22-Dec-14 | 19 |
| L06-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 1 | 09-Dec-14 A | 22-Dec-14 | 17 |
| I-1604 | Manlift finishes - GWB, hang walls | 2 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L07-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L08-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 16-Dec-14 A | |
| L11-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L12-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L14-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L15-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L16-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L17-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |

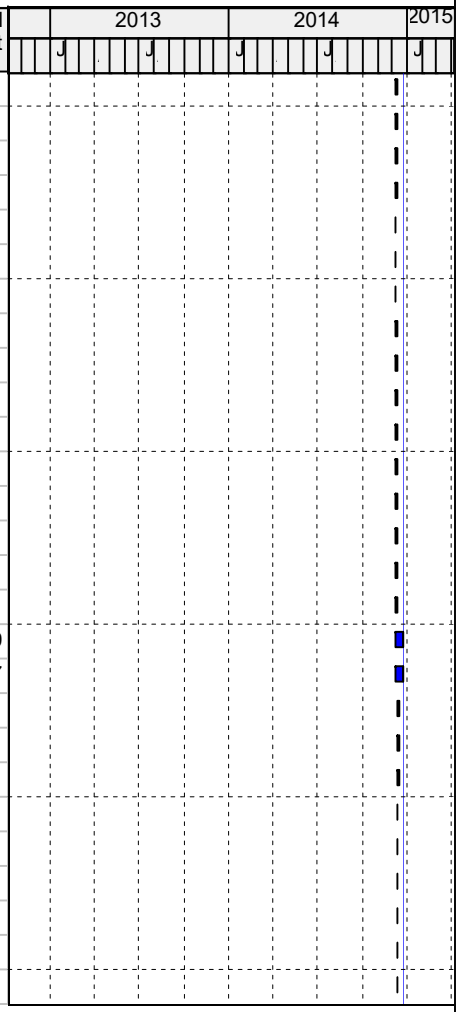



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2E-8340 | LL2 - Install walk-in cooler/freezer (BY OTHERS) | 5 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L10-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 10-Dec-14 A | 17-Dec-14 A | |
| L09-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L10-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L11-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L11-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L12-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L14-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L15-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L16-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L17-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L08-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 1 | 10-Dec-14 A | 22-Dec-14 | 19 |
| I-1634 | Manlift finishes - GWB, hang ceilings | 2 | 0 | 10-Dec-14 A | 16-Dec-14 A | |
| L12-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L14-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L15-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L03-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L04-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| MPT-1018a | (C) Install hi-roof cornice metal | 8 | 0 | 11-Dec-14 A | 20-Dec-14 A | |
| MPT-1034 | (A) Elevation 52 (west elevation, north end, L3-L18) | 4 | 0 | 11-Dec-14 A | 16-Dec-14 A | |
| MPT-1036 | (B) Elevation 45/46 (north elevation, east end, L3-L1 | 5 | 0 | 11-Dec-14 A | 19-Dec-14 A | |
| MPT-1038 | (D) Install louvers, north | 5 | 3 | 11-Dec-14 A | 24-Dec-14 | 21 |
| L16-7030 | Paint | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L17-7030 | Paint | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L05-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L06-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| MPT-1066 | Tower Sign, East (El. 32) - Install backing | 3 | 1 | 12-Dec-14 A | 22-Dec-14 | 35 |

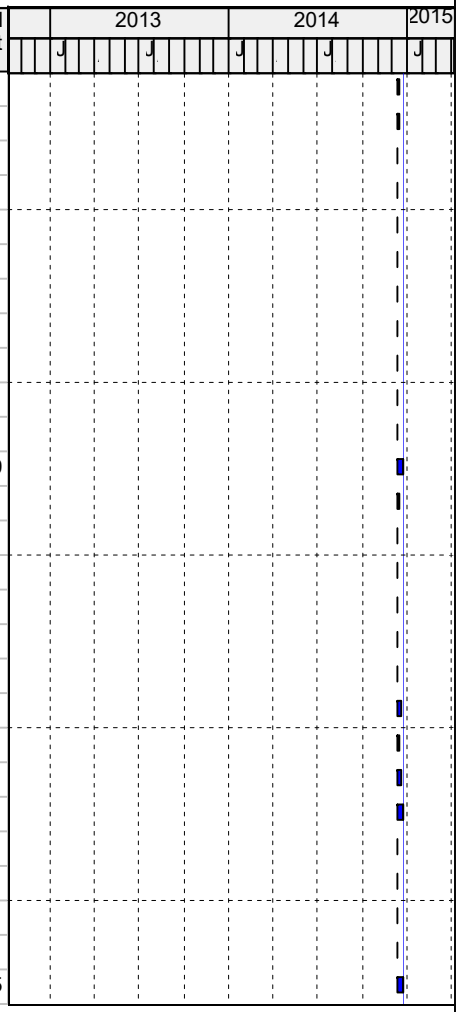



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPT-1076 | (B) Caulking - Elevation 51 (north elevation, west half | 10 | 4 | 12-Dec-14 A | 29-Dec-14 | 17 |
| L04-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L04-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L07-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L08-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L09-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L14-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L15-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L17-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 16-Dec-14 A | |
| L04-7042 | Install Tile Flooring (x41) | 2 | 1 | 15-Dec-14 A | 24-Dec-14 | 45 |
| L05-7042 | Install Tile Flooring (x41) | 2 | 1 | 15-Dec-14 A | 29-Dec-14 | 44 |
| LL4-8102a | LL4 - GWB Tape/Finish | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| LL3-8102a | LL3 - GWB Tape/Finish | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| L03-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L04-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L07-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L08-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L09-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L10-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| CO-7126 | Fire pump test pre-planning complete (see checklist) | 0 | 0 | | 15-Dec-14 A | |
| CO-7214 | Cx - Flush & Fill HVAC Hydronics Systems | 5 | 0 | 15-Dec-14 A | 19-Dec-14 A | |

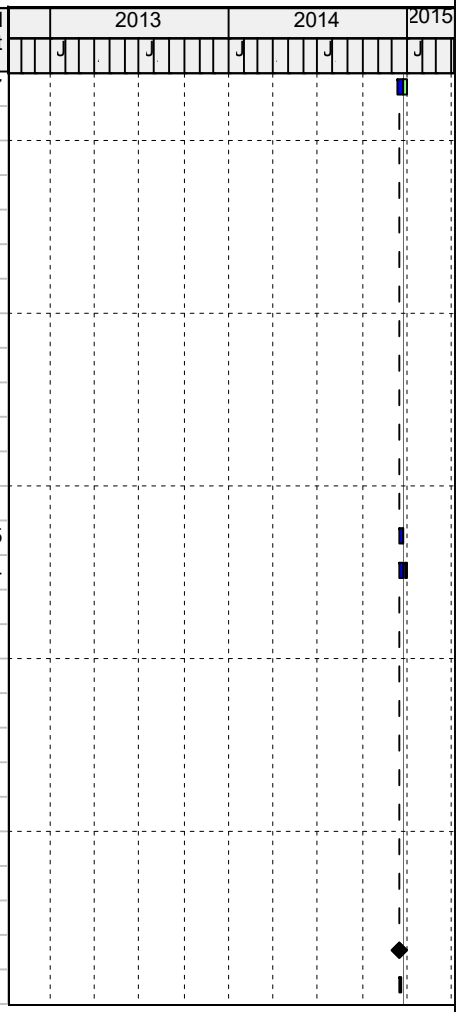



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-6034 | COB Correction - Add ceiling access panels in Food F | 10 | 5 | 15-Dec-14 A | 30-Dec-14 | 15 |
| L03-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| L05-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 16-Dec-14 A | 23-Dec-14 | 18 |
| L09-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L10-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L10-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L11-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L11-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L14-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L15-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L16-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L17-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| LL2E-8342 | LL2 - Final connections at walk-in cooler/freezer | 5 | 1 | 16-Dec-14 A | 22-Dec-14 | 63 |
| L11-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 16-Dec-14 A | 18-Dec-14 A | |
| L16-8201 | Corridors - Install ACT Grid | 2 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L06-7042 | Install Tile Flooring (x41) | 2 | 1 | 16-Dec-14 A | 30-Dec-14 | 41 |
| L07-7042 | Install Tile Flooring (x41) | 2 | 1 | 16-Dec-14 A | 31-Dec-14 | 40 |
| LL1-Z2-8102a | GWB Hang (Ceilings) & Inspection | 3 | 2 | 16-Dec-14 A | 23-Dec-14 | 15 |
| L11-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L14-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L15-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L16-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L17-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| CO-7128 | Run fire pump test | 2 | 0 | 16-Dec-14 A | 17-Dec-14 A | |

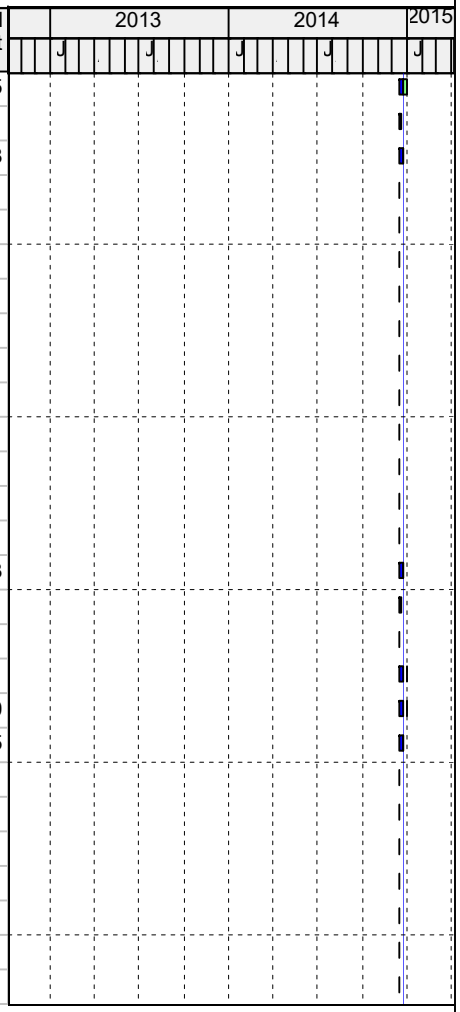



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 1 | 16-Dec-14 A | 22-Dec-14 | 21 |
| SW-2026 | Zone 4 - FRP NW planter | 5 | 3 | 16-Dec-14 A | 07-Jan-15 | 43 |
| L03-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 17-Dec-14 A | 23-Dec-14 | 24 |
| L04-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 17-Dec-14 A | 23-Dec-14 | 16 |
| L06-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 17-Dec-14 A | 23-Dec-14 | 18 |
| L07-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 17-Dec-14 A | 23-Dec-14 | 19 |
| L08-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 17-Dec-14 A | 23-Dec-14 | 19 |
| L09-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 17-Dec-14 A | 23-Dec-14 | 21 |
| L14-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L15-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L16-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L17-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L08-7042 | Install Tile Flooring (x41) | 2 | 1 | 17-Dec-14 A | 02-Jan-15 | 39 |
| L09-7042 | Install Tile Flooring (x41) | 2 | 1 | 17-Dec-14 A | 05-Jan-15 | 38 |
| L04-7136 | Install Door and Hardware | 1 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L16-8216 | Vinyl Wall Coverings - Install Murals | 2 | 1 | 17-Dec-14 A | 22-Dec-14 | 24 |
| MPT-1046 | (A) Elevation 26/27/53 (west elevation, south of 52, L | 3 | 0 | 17-Dec-14 A | 18-Dec-14 A | |
| MPT-1057 | (S) Elevation 32 framing (south elevation, east of mai | 5 | 1 | 17-Dec-14 A | 23-Dec-14 | 35 |
| MPT-1080 | (A) Caulking - Elevation 44 (east elevation above poo | 8 | 5 | 17-Dec-14 A | 30-Dec-14 | 17 |
| LL1-Z2-8108 | Install ceiling clouds | 5 | 4 | 17-Dec-14 A | 30-Dec-14 | 18 |
| MPP-1006 | (C) Install Level 3 cornice metal | 6 | 6 | 18-Dec-14 A | 31-Dec-14 | 28 |
| L10-7042 | Install Tile Flooring (x41) | 2 | 1 | 18-Dec-14 A | 06-Jan-15 | 37 |
| L11-7042 | Install Tile Flooring (x41) | 2 | 1 | 18-Dec-14 A | 24-Dec-14 | 43 |
| LL2-2062 | LL2 - Install ceiling grid | 2 | 2 | 18-Dec-14 A | 23-Dec-14 | 38 |
| MPT-1052 | (A+B) Elevation 48/49 (north elevation, east of 51, L3 | 6 | 6 | 18-Dec-14 A | 31-Dec-14 | 21 |
| L12-7042 | Install Tile Flooring (x41) | 2 | 1 | 19-Dec-14 A | 29-Dec-14 | 42 |
| L14-7042 | Install Tile Flooring (x41) | 2 | 1 | 19-Dec-14 A | 30-Dec-14 | 41 |

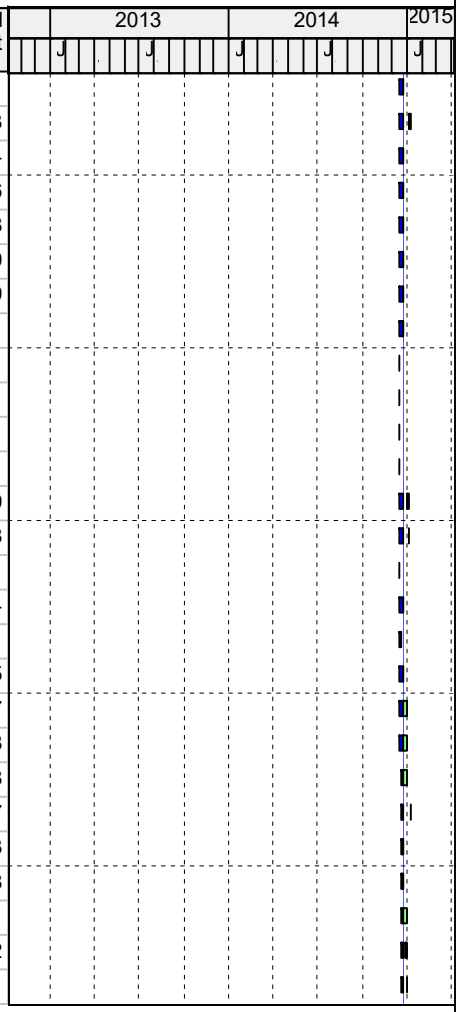



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPT-1048 | (B) Elevation 37 (penthouse east) | 3 | 0 | 19-Dec-14 A | 20-Dec-14 A | |
| I-5000 | Resolve RFI's and site work changes (new drawings) | 10 | 7 | 19-Dec-14 A | 02-Jan-15 | 30 |
| L1BOH2-8215 | GWB Tape (Walls) | 5 | 5 | 22-Dec-14 | 30-Dec-14 | 16 |
| L10-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 21 |
| L11-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 23 |
| L12-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 23 |
| L14-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 25 |
| L15-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 25 |
| L16-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 27 |
| L17-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 27 |
| L1K-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 15 |
| L16-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 22-Dec-14 | 29-Dec-14 | 17 |
| L03-7032 | Install VCT Flooring (x42) | 1 | 1 | 22-Dec-14 | 22-Dec-14 | 41 |
| L04-7032 | Install VCT Flooring (x42) | 1 | 1 | 22-Dec-14 | 22-Dec-14 | 37 |
| L11-7032 | Install VCT Flooring (x42) | 1 | 1 | 22-Dec-14 | 22-Dec-14 | 37 |
| L07-8138 | Bathrooms - Install Toilet Accessories | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 29 |
| L17-8136 | Bathrooms - Install Counter Subtops | 4 | 4 | 22-Dec-14 | 29-Dec-14 | 16 |
| CO-7160 | Generator - Cx generator/owner training | 3 | 3 | 22-Dec-14 | 24-Dec-14 | 66 |
| CO-7212 | Cx - Start-Up Boilers | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 26 |
| CO-7216 | Cx - Start-Up Fluid Cooler | 3 | 3 | 22-Dec-14 | 24-Dec-14 | 21 |
| CO-7234 | Cx - TAB - CW Water Balancing | 10 | 10 | 22-Dec-14 | 07-Jan-15 | 47 |
| L15-8140 | Install window sills | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 21 |
| L14-8140 | Install window sills | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 21 |
| L12-8140 | Install window sills | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 22 |
| L11-8140 | Install window sills | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 22 |
| L16-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 26 |
| L15-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 24 |

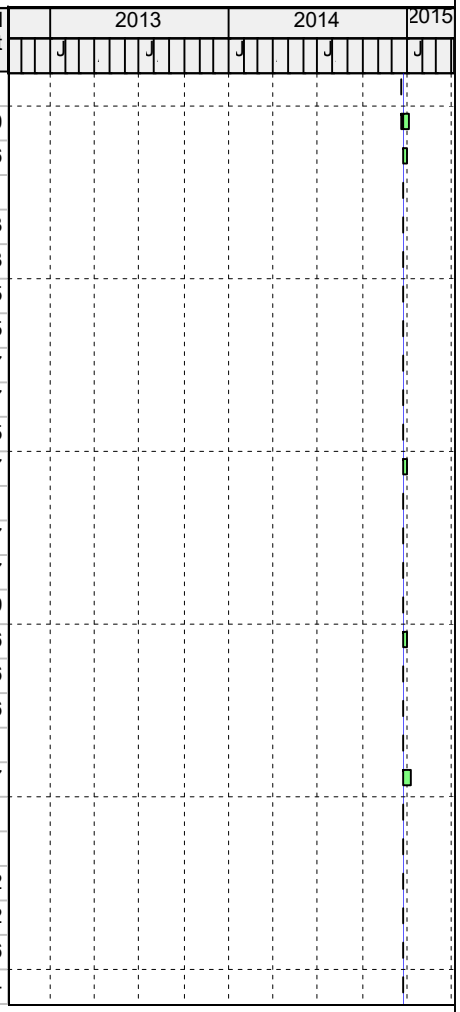


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 24 |
| L12-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 22 |
| L11-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 22 |
| L10-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 20 |
| L05-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 45 |
| L03-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 26 |
| L04-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 45 |
| CO-7252 | Cx - Start-Up - FSD & SD Operation Verification | 10 | 10 | 22-Dec-14* | 07-Jan-15 | 12 |
| SW-2020 | Porte Cochere - Paint | 4 | 4 | 22-Dec-14 | 29-Dec-14 | 34 |
| I-1636 | Manlift finishes - GWB, tape & finish | 5 | 5 | 22-Dec-14 | 30-Dec-14 | 6 |
| L03-8660 | L3 Pool - GWB hang ceilings | 3 | 3 | 22-Dec-14 | 24-Dec-14 | 3 |
| EL-1236 | Elev 1&2 - Walsh/TKE pre-inspection | 6 | 6 | 22-Dec-14 | 31-Dec-14 | 41 |
| EL-6038 | Elev 6 - Rough-in call boxes & lanterns | 5 | 5 | 22-Dec-14 | 30-Dec-14 | 32 |
| EL-6052 | Elev 6 - Complete hoistway ventilation | 5 | 5 | 22-Dec-14 | 30-Dec-14 | 35 |
| LL1-Z3-FCC28 | FCC - Electrical trim/finish | 4 | 4 | 22-Dec-14 | 29-Dec-14 | 28 |
| MPP-1020 | (A+B) Elevation 18/19/21/22 (north elevation, east er | 6 | 6 | 22-Dec-14 | 31-Dec-14 | 20 |
| MPT-1078 | (C) Caulking - Elevation 37/38/39 (penthouse) | 4 | 4 | 22-Dec-14 | 29-Dec-14 | 20 |
| L03-7034 | Install Door and Hardware (x42) | 1 | 1 | 23-Dec-14 | 23-Dec-14 | 41 |
| L04-7034 | Install Door and Hardware (x42) | 1 | 1 | 23-Dec-14 | 23-Dec-14 | 45 |
| L05-7032 | Install VCT Flooring (x42) | 1 | 1 | 23-Dec-14 | 23-Dec-14 | 37 |
| L11-7034 | Install Door and Hardware (x42) | 1 | 1 | 23-Dec-14 | 23-Dec-14 | 43 |
| L12-7032 | Install VCT Flooring (x42) | 1 | 1 | 23-Dec-14 | 23-Dec-14 | 37 |
| L08-8138 | Bathrooms - Install Toilet Accessories | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 29 |
| LL4-8116 | LL4 - Install ACT grid | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 37 |
| LL3-8116 | LL3 - Install ACT grid | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 37 |
| L09-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 44 |
| L08-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 44 |

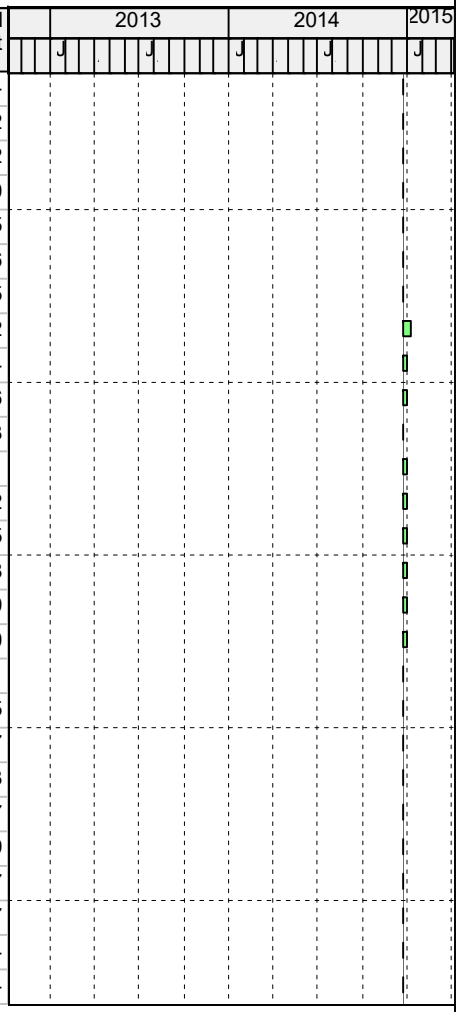



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 44 |
| L06-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 44 |
| L03-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 3 | 24-Dec-14 | 30-Dec-14 | 24 |
| L03-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 1 | 24-Dec-14 | 24-Dec-14 | 26 |
| CO-7102T | Cx - DDC Point-To-Point - Central Plant | 5 | 5 | 24-Dec-14 | 02-Jan-15 | 50 |
| L03-7042 | Install Tile Flooring (x41) | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 41 |
| L03-7138 | Electrical Trim-Out | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 29 |
| L05-7034 | Install Door and Hardware (x42) | 1 | 1 | 24-Dec-14 | 24-Dec-14 | 44 |
| L06-7032 | Install VCT Flooring (x42) | 1 | 1 | 24-Dec-14 | 24-Dec-14 | 37 |
| L12-7034 | Install Door and Hardware (x42) | 1 | 1 | 24-Dec-14 | 24-Dec-14 | 42 |
| L14-7032 | Install VCT Flooring (x42) | 1 | 1 | 24-Dec-14 | 24-Dec-14 | 37 |
| L04-7138 | Electrical Trim-Out | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 23 |
| L05-7138 | Electrical Trim-Out | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 23 |
| L06-7138 | Electrical Trim-Out | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 23 |
| L07-7138 | Electrical Trim-Out | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 23 |
| L08-7138 | Electrical Trim-Out | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 23 |
| L09-7138 | Electrical Trim-Out | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 23 |
| L10-7138 | Electrical Trim-Out | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 23 |
| L11-7138 | Electrical Trim-Out | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 29 |
| L12-7138 | Electrical Trim-Out | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 29 |
| L14-7138 | Electrical Trim-Out | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 29 |
| L15-7138 | Electrical Trim-Out | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 29 |
| L16-7138 | Electrical Trim-Out | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 29 |
| L17-7138 | Electrical Trim-Out | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 29 |
| L09-8138 | Bathrooms - Install Toilet Accessories | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 33 |
| L1K-8102a | GWB Hang (Ceilings at Public Restroom) & Inspectio | 3 | 3 | 24-Dec-14 | 30-Dec-14 | 13 |
| LL2-2088 | LL2 - Install MEP Drops to Grid (including inspection) | 5 | 5 | 24-Dec-14 | 02-Jan-15 | 38 |

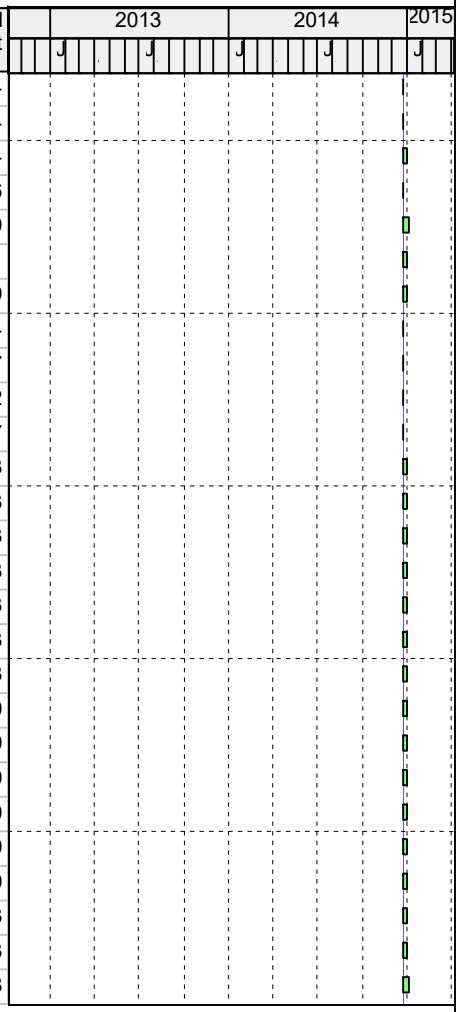



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8216 | Vinyl Wall Coverings - Install Murals | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 21 |
| L16-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 41 |
| L15-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 39 |
| L14-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 39 |
| L12-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 38 |
| L11-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 37 |
| L10-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 43 |
| L03-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 36 |
| CO-7240 | Cx - Heat Pump Start-Up - Levels 3 & 4 | 6 | 6 | 24-Dec-14 | 05-Jan-15 | 26 |
| L03-8662 | L3 Pool - GWB tape ceilings | 3 | 3 | 24-Dec-14 | 27-Dec-14 | 5 |
| L04-7044 | Install Vending Cabinets (x41) | 1 | 1 | 29-Dec-14 | 29-Dec-14 | 45 |
| L06-7034 | Install Door and Hardware (x42) | 1 | 1 | 29-Dec-14 | 29-Dec-14 | 41 |
| L07-7032 | Install VCT Flooring (x42) | 1 | 1 | 29-Dec-14 | 29-Dec-14 | 37 |
| L11-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 29-Dec-14 | 29-Dec-14 | 43 |
| L14-7034 | Install Door and Hardware (x42) | 1 | 1 | 29-Dec-14 | 29-Dec-14 | 41 |
| L15-7032 | Install VCT Flooring (x42) | 1 | 1 | 29-Dec-14 | 29-Dec-14 | 37 |
| L10-8138 | Bathrooms - Install Toilet Accessories | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 33 |
| L02-8130 | L2 - Install ACT Grid | 5 | 5 | 29-Dec-14 | 05-Jan-15 | 21 |
| LL1-Z3-8115 | Install MEP Drops To T Bar Grid Ceiling (including insp | 5 | 5 | 29-Dec-14 | 05-Jan-15 | 12 |
| L16-8140 | Install window sills | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 20 |
| L03-8664 | L3 Pool - Prime & paint ceilings | 3 | 3 | 29-Dec-14 | 31-Dec-14 | 4 |
| L1K-8120 | Install MEP Drops to Grid (including inspection) | 4 | 4 | 29-Dec-14 | 02-Jan-15 | 10 |
| MPT-1050 | (D) Install louvers, east | 4 | 4 | 29-Dec-14 | 02-Jan-15 | 21 |
| L1BOH2-8104 | Prime Paint | 4 | 4 | 30-Dec-14 | 03-Jan-15 | 19 |
| L12-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 30-Dec-14 | 05-Jan-15 | 34 |
| L03-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 30-Dec-14 | 30-Dec-14 | 41 |
| L05-7044 | Install Vending Cabinets (x41) | 1 | 1 | 30-Dec-14 | 30-Dec-14 | 44 |

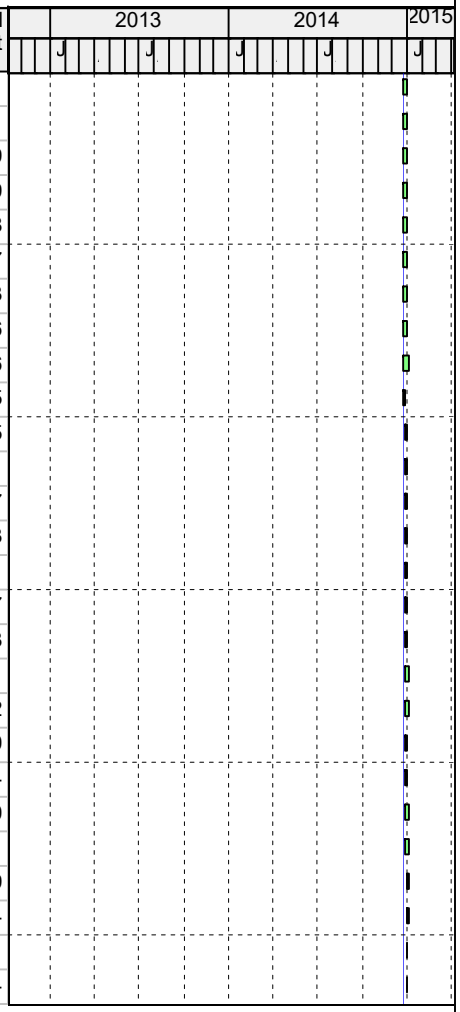



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7034 | Install Door and Hardware (x42) | 1 | 1 | 30-Dec-14 | 30-Dec-14 | 40 |
| L08-7032 | Install VCT Flooring (x42) | 1 | 1 | 30-Dec-14 | 30-Dec-14 | 37 |
| L12-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 30-Dec-14 | 30-Dec-14 | 42 |
| L15-7034 | Install Door and Hardware (x42) | 1 | 1 | 30-Dec-14 | 30-Dec-14 | 39 |
| L16-7032 | Install VCT Flooring (x42) | 1 | 1 | 30-Dec-14 | 30-Dec-14 | 37 |
| L11-8138 | Bathrooms - Install Toilet Accessories | 2 | 2 | 30-Dec-14 | 31-Dec-14 | 33 |
| CO-7222 | Cx - Start-Up - Kitchen Exhaust Fans | 2 | 2 | 30-Dec-14 | 31-Dec-14 | 29 |
| LL1-8120 | Install MEP Drops To T Bar Grid Ceiling | 3 | 3 | 30-Dec-14 | 02-Jan-15 | 18 |
| CO-7262 | Cx - Start-Up - Electric Unit Heaters | 3 | 3 | 30-Dec-14 | 02-Jan-15 | 48 |
| SW-2022 | Remove pedestrian protection on 10th Ave | 1 | 1 | 30-Dec-14 | 30-Dec-14 | 34 |
| LL1-Z3-FCC30 | FCC - Data/phone trim/finish | 4 | 4 | 30-Dec-14 | 05-Jan-15 | 28 |
| MPT-1082 | (C) Caulking - Elevation 48/49 (north elevation, east c | 4 | 4 | 30-Dec-14 | 05-Jan-15 | 20 |
| MPT-1088 | (B) Caulking - Elevation 52/53/26/27 (west elevation, | 11 | 11 | 30-Dec-14 | 14-Jan-15 | 17 |
| I-1606 | Manlift finishes - Prime & paint | 4 | 4 | 31-Dec-14 | 06-Jan-15 | 6 |
| LL1-6014Ib | L1 bar redesign - rework ceiling framing & inspection | 5 | 5 | 31-Dec-14 | 07-Jan-15 | 7 |
| L17-8121 | Install Bathroom "Barn Doors" | 4 | 4 | 31-Dec-14 | 06-Jan-15 | 16 |
| L06-7044 | Install Vending Cabinets (x41) | 1 | 1 | 31-Dec-14 | 31-Dec-14 | 41 |
| L08-7034 | Install Door and Hardware (x42) | 1 | 1 | 31-Dec-14 | 31-Dec-14 | 39 |
| L09-7032 | Install VCT Flooring (x42) | 1 | 1 | 31-Dec-14 | 31-Dec-14 | 37 |
| L14-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 31-Dec-14 | 31-Dec-14 | 41 |
| L15-7042 | Install Tile Flooring (x41) | 2 | 2 | 31-Dec-14 | 02-Jan-15 | 39 |
| L16-7034 | Install Door and Hardware (x42) | 1 | 1 | 31-Dec-14 | 31-Dec-14 | 38 |
| L17-7032 | Install VCT Flooring (x42) | 1 | 1 | 31-Dec-14 | 31-Dec-14 | 37 |
| L12-8138 | Bathrooms - Install Toilet Accessories | 2 | 2 | 31-Dec-14 | 02-Jan-15 | 33 |
| L17-8218 | Corridors - Fire Sprinkler Trim | 2 | 2 | 31-Dec-14 | 02-Jan-15 | 19 |
| SW-2046 | Zone 4 - Install site lighting | 7 | 7 | 31-Dec-14 | 09-Jan-15 | 38 |
| EL-6040 | Elev 6 - Install machine room controller equipment/hy | 3 | 3 | 31-Dec-14 | 05-Jan-15 | 32 |

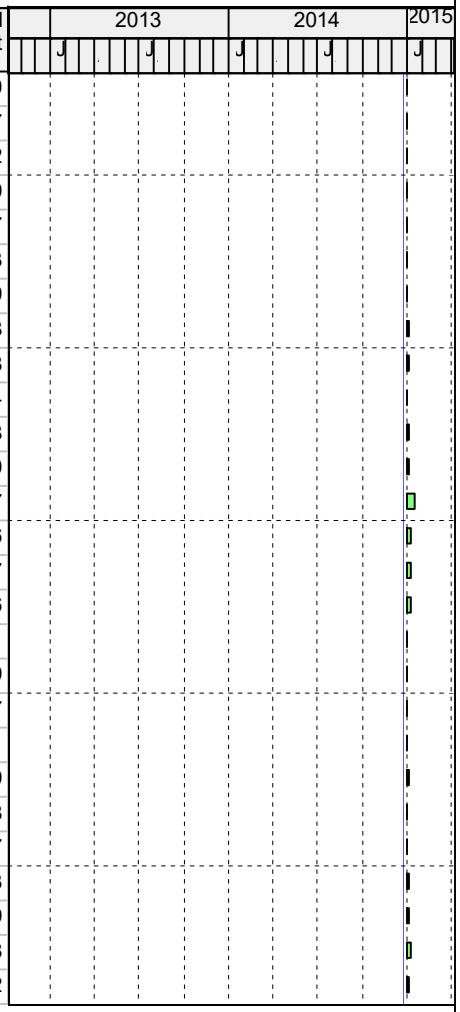



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6042 | Elev 6 - Install EMR heat pump | 6 | 6 | 31-Dec-14 | 08-Jan-15 | 32 |
| EL-6054 | Elev 6 - Install EMR doors, hardware & labeling | 2 | 2 | 31-Dec-14 | 02-Jan-15 | 35 |
| LL1-Z3-6036 | GWB Hang/Tape Ceiling at Food Prep (Dry Storage) | 4 | 4 | 31-Dec-14 | 06-Jan-15 | 15 |
| L1K-8102b | GWB Tape/Finish at Restrooms | 5 | 5 | 31-Dec-14 | 07-Jan-15 | 13 |
| MPT-1084 | (A) Caulking - Hi-roof cornice metal | 6 | 6 | 31-Dec-14 | 08-Jan-15 | 18 |
| MPT-1086 | (A) Caulking - Elevation 45/46 (north elevation, east e | 7 | 7 | 31-Dec-14 | 09-Jan-15 | 17 |
| MPP-1004 | (C) Pool Area cornice metal | 3 | 3 | 02-Jan-15 | 06-Jan-15 | 28 |
| L03-8622 | L3 Pool - HVAC trim / Finish | 2 | 2 | 02-Jan-15 | 05-Jan-15 | 4 |
| L03-8624 | L3 Pool - Fire Sprinkler Trim / Finish | 2 | 2 | 02-Jan-15 | 05-Jan-15 | 4 |
| L07-7044 | Install Vending Cabinets (x41) | 1 | 1 | 02-Jan-15 | 02-Jan-15 | 40 |
| L09-7034 | Install Door and Hardware (x42) | 1 | 1 | 02-Jan-15 | 02-Jan-15 | 38 |
| L10-7032 | Install VCT Flooring (x42) | 1 | 1 | 02-Jan-15 | 02-Jan-15 | 37 |
| L16-7042 | Install Tile Flooring (x41) | 2 | 2 | 02-Jan-15 | 05-Jan-15 | 38 |
| L17-7034 | Install Door and Hardware (x42) | 1 | 1 | 02-Jan-15 | 02-Jan-15 | 37 |
| LL1-Z2-8115 | Install MEP Drops To T Bar Grid Ceiling | 3 | 3 | 02-Jan-15 | 06-Jan-15 | 15 |
| CO-7256 | Cx - Start-Up - Elevator Machine Room Ductless Split | 1 | 1 | 02-Jan-15 | 02-Jan-15 | 29 |
| MPP-1022 | (B) Complete Elevation 40 (pool south elevation, L3-L | 2 | 2 | 02-Jan-15 | 05-Jan-15 | 20 |
| MPP-1026 | (A) Complete Elevation 7/8 (east elevation) | 5 | 5 | 02-Jan-15 | 08-Jan-15 | 21 |
| L1K-8124a | Install Flooring (Epoxy) | 14 | 14 | 03-Jan-15 | 19-Jan-15 | 12 |
| L1BOH2-8114 | T Bar Grid Ceiling | 3 | 3 | 05-Jan-15 | 07-Jan-15 | 15 |
| L08-7044 | Install Vending Cabinets (x41) | 1 | 1 | 05-Jan-15 | 05-Jan-15 | 39 |
| L10-7034 | Install Door and Hardware (x42) | 1 | 1 | 05-Jan-15 | 05-Jan-15 | 37 |
| L15-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 05-Jan-15 | 05-Jan-15 | 39 |
| L17-7042 | Install Tile Flooring (x41) | 2 | 2 | 05-Jan-15 | 06-Jan-15 | 37 |
| CO-7226 | Cx - Start-Up - Misc. Equipment | 5 | 5 | 05-Jan-15 | 09-Jan-15 | 48 |
| LL2-2094 | LL2 - Install doors & hardware | 1 | 1 | 05-Jan-15 | 05-Jan-15 | 38 |
| L17-8140 | Install window sills | 2 | 2 | 05-Jan-15 | 06-Jan-15 | 16 |

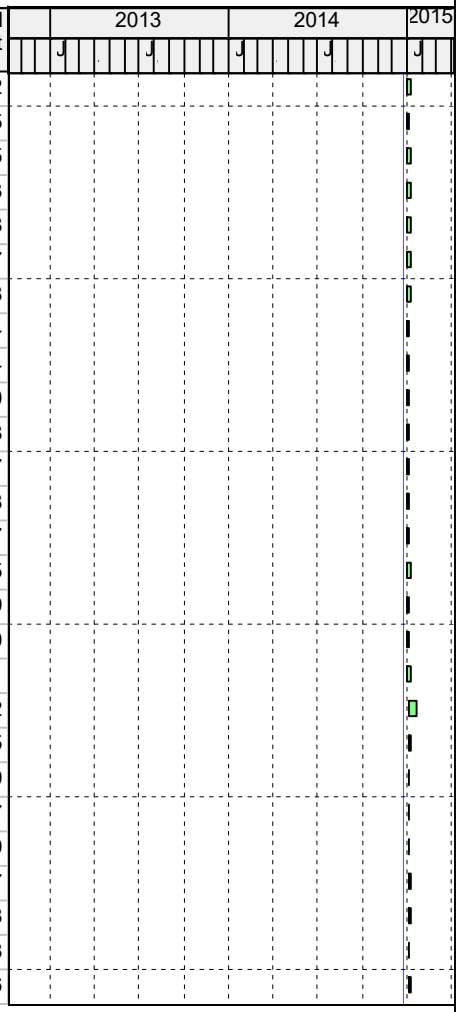



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 2 | 05-Jan-15 | 06-Jan-15 | 19 |
| LL1-Z3-8142 | Install Restroom Ceramic Tile | 5 | 5 | 05-Jan-15 | 09-Jan-15 | 29 |
| SW-2030 | Zone 4 - Remove existing trees | 1 | 1 | 05-Jan-15 | 05-Jan-15 | 31 |
| SW-2032 | Zone 4 - Demo existing hardscapes | 3 | 3 | 05-Jan-15 | 07-Jan-15 | 31 |
| L03-8666 | L3 Pool - Elec Trim / Finish at ceiling | 2 | 2 | 05-Jan-15 | 06-Jan-15 | 4 |
| LL1-Z3-8202 | Install FRP | 5 | 5 | 05-Jan-15 | 09-Jan-15 | 12 |
| MPT-1068 | Tower Sign, North (El. 51) | 5 | 5 | 05-Jan-15* | 09-Jan-15 | 37 |
| CO-7100T | Cx - Start-Up - Life Safety Exhaust Fans and VFD's | 12 | 12 | 06-Jan-15 | 21-Jan-15 | 16 |
| L14-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 06-Jan-15 | 09-Jan-15 | 31 |
| L15-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 06-Jan-15 | 09-Jan-15 | 31 |
| L09-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 06-Jan-15 | 06-Jan-15 | 38 |
| L16-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 06-Jan-15 | 06-Jan-15 | 38 |
| L14-8138 | Bathrooms - Install Toilet Accessories | 2 | 2 | 06-Jan-15 | 07-Jan-15 | 31 |
| SW-2314 | Zone 3 - FRP sidewalk | 4 | 4 | 06-Jan-15 | 09-Jan-15 | 32 |
| LL2-2086 | LL2 - Epoxy Flooring at Laundry Room | 7 | 7 | 06-Jan-15 | 14-Jan-15 | 38 |
| CO-7242 | Cx - Heat Pump Start-Up - Levels 5 & 6 | 5 | 5 | 06-Jan-15 | 12-Jan-15 | 26 |
| SW-2034 | Zone 4 - Install irrigation sleeves | 3 | 3 | 06-Jan-15 | 08-Jan-15 | 33 |
| I-1638 | Manlift finishes - Install ceiling grid | 3 | 3 | 06-Jan-15 | 08-Jan-15 | 7 |
| I-1640 | Manlift finishes - Install window sills | 3 | 3 | 06-Jan-15 | 08-Jan-15 | 53 |
| L03-8670 | L3 Pool - Rough-in pool trench drain | 4 | 4 | 06-Jan-15 | 09-Jan-15 | 4 |
| EL-6044 | Elev 6 - Electrical trim | 3 | 3 | 06-Jan-15 | 08-Jan-15 | 32 |
| EL-6046 | Elev 6 - Fire alarm trim | 3 | 3 | 06-Jan-15 | 08-Jan-15 | 32 |
| EL-6048 | Elev 6 - Fire sprinkler trim | 3 | 3 | 06-Jan-15 | 08-Jan-15 | 32 |
| EL-6050 | Elev 6 - Install pit grates | 3 | 3 | 06-Jan-15 | 08-Jan-15 | 32 |
| LL1-Z3-FCC32 | FCC - Install flooring & base | 3 | 3 | 06-Jan-15 | 08-Jan-15 | 28 |
| MPP-1024 | (B) Complete Elevation 4 (south elevation, east of tov | 1 | 1 | 06-Jan-15 | 06-Jan-15 | 27 |
| MPT-1090 | (C) Caulking - Elevation 40 (pool south elevation, L3-I | 9 | 9 | 06-Jan-15 | 16-Jan-15 | 20 |

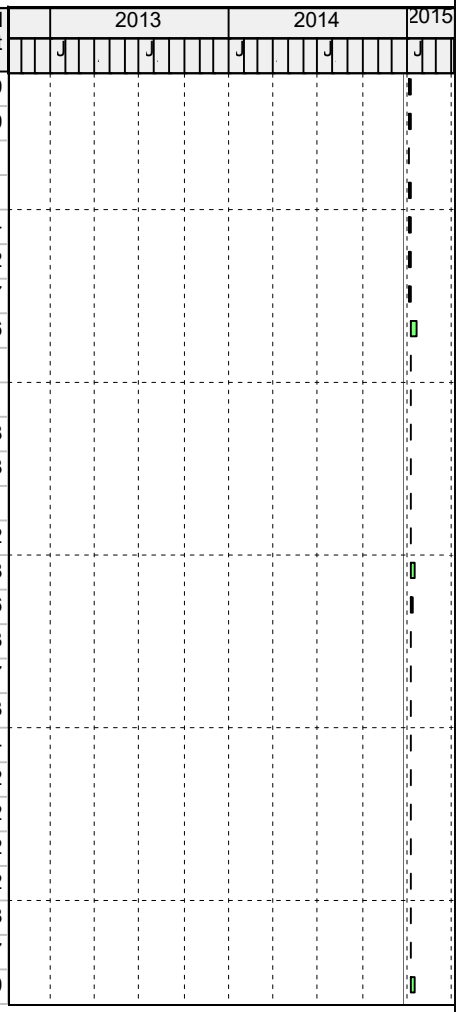



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 07-Jan-15 | 07-Jan-15 | 37 |
| L17-7044 | Install Guest Laundry Equipment (x41) | 1 | 1 | 07-Jan-15 | 07-Jan-15 | 37 |
| L15-8138 | Bathrooms - Install Toilet Accessories | 2 | 2 | 07-Jan-15 | 08-Jan-15 | 31 |
| L17-8224 | Corridors - HVAC Grilles & Registers | 2 | 2 | 07-Jan-15 | 08-Jan-15 | 33 |
| L1BOH2C-6024 | MEP Trim at Ceiling | 3 | 3 | 07-Jan-15 | 09-Jan-15 | 15 |
| L03-8668 | L3 Pool - Remove scaffolding at pool pit | 1 | 1 | 07-Jan-15 | 07-Jan-15 | 4 |
| MPT-1054 | (B) Elevation 3/30 (south elevation, west of manlift, L | 5 | 5 | 07-Jan-15 | 13-Jan-15 | 27 |
| MPP-1028 | (C) Tapered pilasters, west | 3 | 3 | 07-Jan-15 | 09-Jan-15 | 36 |
| L1BOH2-8140 | Acoustical Ceiling Tile | 2 | 2 | 08-Jan-15 | 09-Jan-15 | 15 |
| LL1-6014Ib2 | L1 bar redesign - GWB hang at ceilings | 4 | 4 | 08-Jan-15 | 13-Jan-15 | 7 |
| CO-7232 | Cx - TAB - CW Pump Totalization | 1 | 1 | 08-Jan-15 | 08-Jan-15 | 46 |
| CO-7254 | Cx - Start-Up - MUA AAON (8) | 8 | 8 | 08-Jan-15 | 19-Jan-15 | 12 |
| SW-2036 | Zone 4 - Grade for curb and gutter | 1 | 1 | 08-Jan-15 | 08-Jan-15 | 31 |
| L03-8672 | L3 Pool - Prep pool area for topping slab | 2 | 2 | 08-Jan-15 | 09-Jan-15 | 4 |
| SW-2220 | Zone 2 - FRP curb/gutter at NW corner | 4 | 4 | 08-Jan-15 | 13-Jan-15 | 30 |
| L16-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 09-Jan-15 | 14-Jan-15 | 30 |
| L16-8138 | Bathrooms - Install Toilet Accessories | 2 | 2 | 09-Jan-15 | 12-Jan-15 | 30 |
| L1B-8102a | GWB Hang (Ceilings) | 5 | 5 | 09-Jan-15 | 15-Jan-15 | 5 |
| SW-2038 | Zone 4 - FRP curb & gutter | 1 | 1 | 09-Jan-15 | 09-Jan-15 | 31 |
| LL1-Z3-FCC34 | FCC - Final paint/touch up | 2 | 2 | 09-Jan-15 | 12-Jan-15 | 28 |
| LL1-Z3-FCC36 | FCC - Install door & hardware | 2 | 2 | 09-Jan-15 | 12-Jan-15 | 28 |
| MPP-1032 | (A) Elevation 1/A/B/C/23/24/25 (Porte Cochere, belov | 5 | 5 | 09-Jan-15 | 15-Jan-15 | 21 |
| L1BOH2-8200 | First Coat Finish Paint | 5 | 5 | 12-Jan-15 | 16-Jan-15 | 15 |
| SW-2322 | Zone 3 - Install irrigation | 5 | 5 | 12-Jan-15 | 16-Jan-15 | 52 |
| SW-2324 | Zone 3 - Install landscaping | 5 | 5 | 12-Jan-15 | 16-Jan-15 | 52 |
| CO-7400 | Cx - 3rd Party Cx of Mechanical, Plumbing, Electrical | 45 | 45 | 12-Jan-15 | 13-Mar-15 | 12 |
| LL1-Z3-8144 | Install Restroom Fixtures | 5 | 5 | 12-Jan-15 | 16-Jan-15 | 29 |

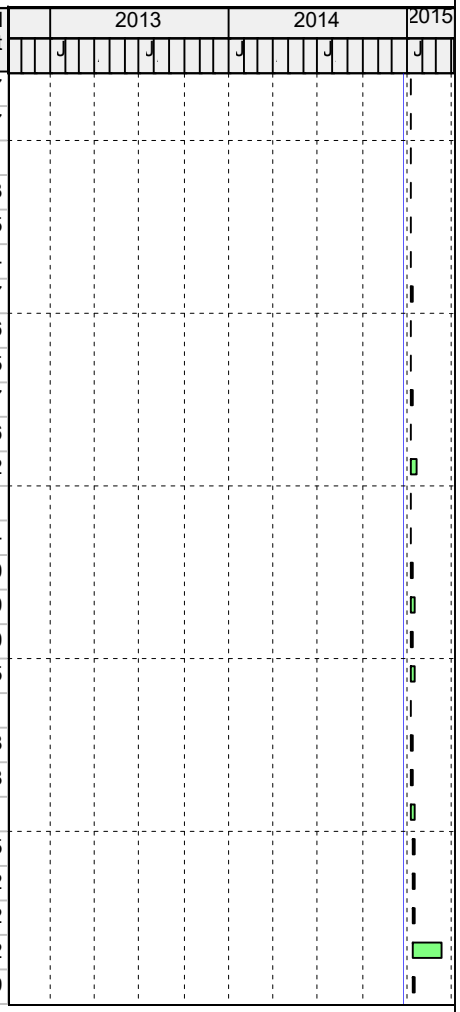



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8648 | L3 Pool- Install pool topping slab | 1 | 1 | 12-Jan-15 | 12-Jan-15 | 4 |
| SW-2040 | Zone 4 - Grade for sidewalk | 7 | 7 | 12-Jan-15 | 20-Jan-15 | 31 |
| MPP-1030 | (C) Tapered pilasters, east | 3 | 3 | 12-Jan-15 | 14-Jan-15 | 36 |
| MPT-1070 | Tower Sign, East (El. 44) | 5 | 5 | 12-Jan-15 | 16-Jan-15 | 37 |
| MPP-1040 | (A+B) Caulking - Pool area | 8 | 8 | 12-Jan-15 | 21-Jan-15 | 17 |
| L03-8612 | L3 Pool - GWB hang/tape/finish | 6 | 6 | 13-Jan-15 | 20-Jan-15 | 4 |
| LL1-Z2-8124a | Install Base | 3 | 3 | 13-Jan-15 | 15-Jan-15 | 15 |
| L02-8138 | L2 - Install ceiling tile | 2 | 2 | 13-Jan-15 | 14-Jan-15 | 21 |
| CO-7244 | Cx - Heat Pump Start-Up - Levels 7 & 8 | 5 | 5 | 13-Jan-15 | 19-Jan-15 | 26 |
| LL1-Z3-FCC38 | FCC - Final clean and punch list | 3 | 3 | 13-Jan-15 | 15-Jan-15 | 28 |
| L04-8418 | Flooring at Elevator Lobby | 2 | 2 | 14-Jan-15 | 15-Jan-15 | 4 |
| L1L-8102a | GWB Tape (Walls & Ceilings) | 12 | 12 | 14-Jan-15 | 29-Jan-15 | 0 |
| SW-2212 | Zone 2 - FRP sidewalk | 3 | 3 | 14-Jan-15 | 16-Jan-15 | 30 |
| LL1-6014Id | L1 bar redesign - Complete finishes at ceilings | 5 | 5 | 14-Jan-15 | 20-Jan-15 | 7 |
| MPT-1056 | (B) Complete Elevation 31 (above L12 terrace, west e | 4 | 4 | 14-Jan-15 | 19-Jan-15 | 27 |
| L04-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 15-Jan-15 | 15-Jan-15 | 6 |
| LL2-2048 | LL2 - Set Laundry Room equipment (BY OTHERS) | 2 | 2 | 15-Jan-15 | 16-Jan-15 | 38 |
| L17-8129 | Bathrooms - Install Shower Doors | 4 | 4 | 15-Jan-15 | 20-Jan-15 | 25 |
| L17-8138 | Bathrooms - Install Toilet Accessories | 2 | 2 | 15-Jan-15 | 16-Jan-15 | 27 |
| MPP-1034 | (C) Porte Cochere cornice metal | 3 | 3 | 15-Jan-15 | 19-Jan-15 | 36 |
| I-3102 | Ballroom ceilings - additional work per ASIs 18, 25 (cl | 7 | 7 | 16-Jan-15 | 26-Jan-15 | 5 |
| L04-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 16-Jan-15 | 19-Jan-15 | 29 |
| L05-8418 | Flooring at Elevator Lobby | 2 | 2 | 16-Jan-15 | 19-Jan-15 | 4 |
| L06-8418 | Flooring at Elevator Lobby | 2 | 2 | 16-Jan-15 | 19-Jan-15 | 4 |
| SW-2042 | Zone 4 - Install trench drain | 3 | 3 | 16-Jan-15 | 20-Jan-15 | 31 |
| LL1-Z3-FCC40 | FCC - Install Knox Box | 2 | 2 | 16-Jan-15 | 19-Jan-15 | 28 |
| MPT-1058 | (A) Elevation 32 hat channel (south elevation, east of | 3 | 3 | 16-Jan-15 | 20-Jan-15 | 21 |

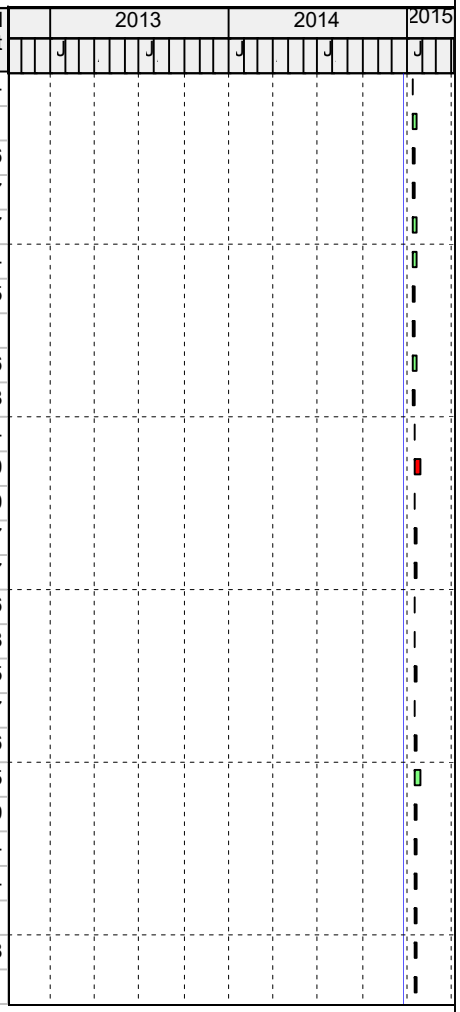



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7414 | Cx - Pressure Testing - Elevators Complete / Recall Te | 0 | 0 | | 16-Jan-15 | 35 |
| L1BOH2-8124 | Flooring | 5 | 5 | 19-Jan-15 | 23-Jan-15 | 15 |
| L05-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 19-Jan-15 | 19-Jan-15 | 5 |
| L06-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 19-Jan-15 | 19-Jan-15 | 5 |
| LL2-2050 | LL2 - Laundry Room equipment final connections (MI | 1 | 1 | 19-Jan-15 | 19-Jan-15 | 38 |
| L03-8644 | L3 Pool - Connect, startup & adjust pool equipment | 10 | 10 | 19-Jan-15 | 30-Jan-15 | 36 |
| SW-2118 | Zone 1 - FRP sidewalk | 3 | 3 | 19-Jan-15 | 21-Jan-15 | 30 |
| MPP-1012 | (C) Caulking - Elevation 4 (south elevation, east of to\ | 6 | 6 | 19-Jan-15 | 26-Jan-15 | 20 |
| LL2-2090 | LL2 - Install ceiling tile | 1 | 1 | 19-Jan-15 | 19-Jan-15 | 39 |
| LL1-Z3-8146 | Install Restroom Accessories | 2 | 2 | 19-Jan-15 | 20-Jan-15 | 29 |
| MPT-1072 | Tower Sign, West (El, 52) | 5 | 5 | 19-Jan-15 | 23-Jan-15 | 37 |
| L05-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 20-Jan-15 | 21-Jan-15 | 27 |
| L06-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 20-Jan-15 | 21-Jan-15 | 27 |
| L07-8418 | Flooring at Elevator Lobby | 2 | 2 | 20-Jan-15 | 21-Jan-15 | 3 |
| L08-8418 | Flooring at Elevator Lobby | 2 | 2 | 20-Jan-15 | 21-Jan-15 | 3 |
| L1K-8128 | Install Kitchen equipment (BY OTHERS) | 5 | 5 | 20-Jan-15 | 26-Jan-15 | 10 |
| L04-7140 | Fire Alarm Trim (Install Devices) | 1 | 1 | 20-Jan-15 | 20-Jan-15 | 7 |
| LL1-Z3-FCC22 | FCC - Final inspections by CoB and Fire Marshall | 2 | 2 | 20-Jan-15 | 21-Jan-15 | 28 |
| LL2-2092 | LL2 - MEP trim | 3 | 3 | 20-Jan-15 | 22-Jan-15 | 38 |
| L04-8222 | Corridors - Fire Alarm Trim (Install Devices) | 1 | 1 | 20-Jan-15 | 20-Jan-15 | 4 |
| CO-7246 | Cx - Heat Pump Start-Up - Levels 9 & 10 | 5 | 5 | 20-Jan-15 | 26-Jan-15 | 26 |
| CO-7258 | Cx - Start-Up - KMUA Trane (2) | 1 | 1 | 20-Jan-15 | 20-Jan-15 | 12 |
| MPT-1060 | (B) Elevation 33/34 hat channel (east elevation, soutl | 3 | 3 | 20-Jan-15 | 22-Jan-15 | 27 |
| L04-8420 | Fire Alarm Trim (Install Devices) | 1 | 1 | 20-Jan-15 | 20-Jan-15 | 4 |
| L07-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 21-Jan-15 | 21-Jan-15 | 4 |
| L08-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 21-Jan-15 | 21-Jan-15 | 4 |
| LL1-Z3-8340 | Install walk-in cooler/freezer (BY OTHERS) | 5 | 5 | 21-Jan-15* | 27-Jan-15 | 22 |

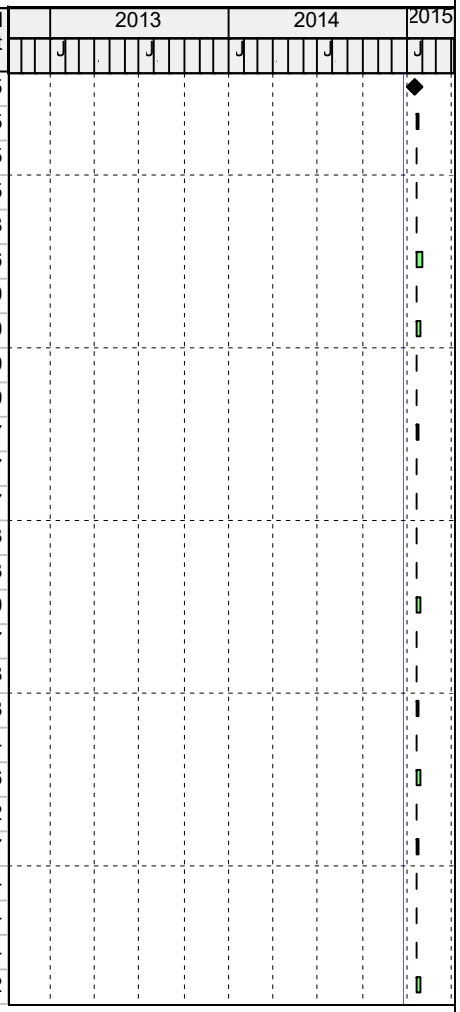



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8614 | L3 Pool - Paint/wall finishes | 3 | 3 | 21-Jan-15 | 23-Jan-15 | 4 |
| L04-7134 | Install VCT Flooring | 2 | 2 | 21-Jan-15 | 22-Jan-15 | 17 |
| L05-7140 | Fire Alarm Trim (Install Devices) | 1 | 1 | 21-Jan-15 | 21-Jan-15 | 6 |
| L06-7140 | Fire Alarm Trim (Install Devices) | 1 | 1 | 21-Jan-15 | 21-Jan-15 | 6 |
| L1BOH2-8124a | Install Base | 3 | 3 | 21-Jan-15 | 23-Jan-15 | 16 |
| CO-7220 | Cx - Start-Up - Common Space Heat Pump | 4 | 4 | 21-Jan-15 | 26-Jan-15 | 12 |
| L1K-8210 | Install Restroom Ceramic Tile | 5 | 5 | 21-Jan-15 | 27-Jan-15 | 13 |
| L06-8222 | Corridors - Fire Alarm Trim (Install Devices) | 1 | 1 | 21-Jan-15 | 21-Jan-15 | 4 |
| L05-8222 | Corridors - Fire Alarm Trim (Install Devices) | 1 | 1 | 21-Jan-15 | 21-Jan-15 | 4 |
| CO-7260 | Cx - Start-Up - Ballroom AAON RTU | 1 | 1 | 21-Jan-15 | 21-Jan-15 | 29 |
| MPT-1062 | (A) Elevation 32 metal panels (south elevation, east c | 8 | 8 | 21-Jan-15 | 30-Jan-15 | 21 |
| L05-8420 | Fire Alarm Trim (Install Devices) | 1 | 1 | 21-Jan-15 | 21-Jan-15 | 4 |
| L06-8420 | Fire Alarm Trim (Install Devices) | 1 | 1 | 21-Jan-15 | 21-Jan-15 | 4 |
| L07-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 22-Jan-15 | 23-Jan-15 | 25 |
| L08-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 22-Jan-15 | 23-Jan-15 | 25 |
| L09-8418 | Flooring at Elevator Lobby | 2 | 2 | 22-Jan-15 | 23-Jan-15 | 3 |
| L10-8418 | Flooring at Elevator Lobby | 2 | 2 | 22-Jan-15 | 23-Jan-15 | 3 |
| L05-7134 | Install VCT Flooring | 2 | 2 | 22-Jan-15 | 23-Jan-15 | 17 |
| L07-7140 | Fire Alarm Trim (Install Devices) | 1 | 1 | 22-Jan-15 | 22-Jan-15 | 5 |
| L08-7140 | Fire Alarm Trim (Install Devices) | 1 | 1 | 22-Jan-15 | 22-Jan-15 | 5 |
| LL1-8124a | Install Base | 5 | 5 | 22-Jan-15 | 28-Jan-15 | 7 |
| SW-2120 | Zone 1 - Install irrigation | 5 | 5 | 22-Jan-15 | 28-Jan-15 | 41 |
| SW-2122 | Zone 1 - Install landscaping | 5 | 5 | 22-Jan-15 | 28-Jan-15 | 41 |
| MPP-1016 | (A+B) Caulking - Elevation 7/8 (east elevation) | 8 | 8 | 22-Jan-15 | 02-Feb-15 | 17 |
| L08-8222 | Corridors - Fire Alarm Trim (Install Devices) | 1 | 1 | 22-Jan-15 | 22-Jan-15 | 4 |
| L07-8222 | Corridors - Fire Alarm Trim (Install Devices) | 1 | 1 | 22-Jan-15 | 22-Jan-15 | 4 |
| CO-7264 | Cx - Start-Up - Lobby Trane TRU (2) | 2 | 2 | 22-Jan-15 | 23-Jan-15 | 37 |

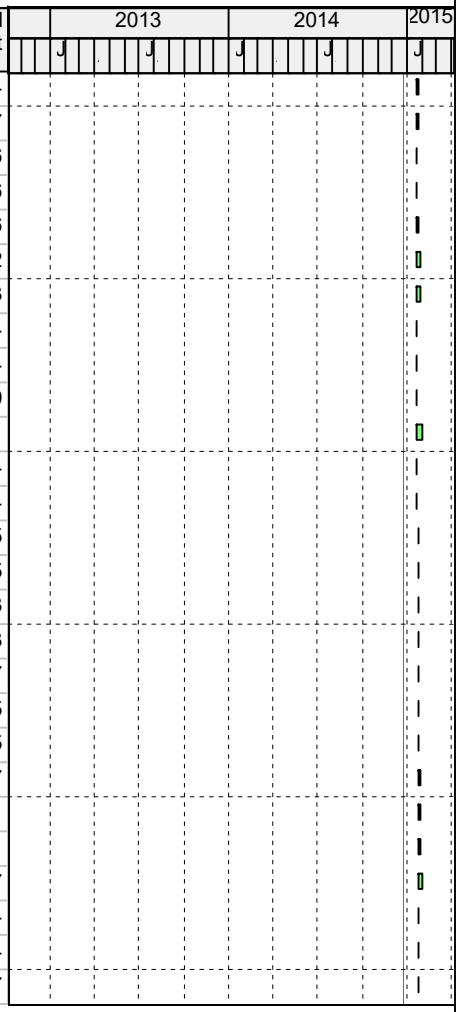



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7132 | Cx - DDC Point-To-Point - Ballroom VAV | 1 | 1 | 22-Jan-15 | 22-Jan-15 | 29 |
| SW-2044 | Zone 4 - FRP sidewalk | 4 | 4 | 22-Jan-15 | 27-Jan-15 | 30 |
| MPT-1064 | (B) Elevation 33/34 metal panels (east elevation, sou | 7 | 7 | 22-Jan-15 | 30-Jan-15 | 27 |
| MPP-1046 | (A+B) Caulking - Elevation 5/6 (east elevation, south | 8 | 8 | 22-Jan-15 | 02-Feb-15 | 17 |
| L07-8420 | Fire Alarm Trim (Install Devices) | 1 | 1 | 22-Jan-15 | 22-Jan-15 | 4 |
| L08-8420 | Fire Alarm Trim (Install Devices) | 1 | 1 | 22-Jan-15 | 22-Jan-15 | 4 |
| L09-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 23-Jan-15 | 23-Jan-15 | 3 |
| L10-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 23-Jan-15 | 23-Jan-15 | 3 |
| L06-7134 | Install VCT Flooring | 2 | 2 | 23-Jan-15 | 26-Jan-15 | 17 |
| L03-8640 | L3 Pool - Prep and install plaster | 3 | 3 | 23-Jan-15 | 27-Jan-15 | 4 |
| L04-7146 | Final Coat Finish Paint | 2 | 2 | 23-Jan-15 | 26-Jan-15 | 24 |
| CO-7134 | Cx - DDC Point-To-Point - Ballroom RTU (2) | 2 | 2 | 23-Jan-15 | 26-Jan-15 | 29 |
| L1BOH2-8116 | Finish Carpentry / Millwork | 5 | 5 | 26-Jan-15 | 30-Jan-15 | 15 |
| L1BOH2-8126 | Doors & Hardware | 5 | 5 | 26-Jan-15 | 30-Jan-15 | 16 |
| L09-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 23 |
| L10-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 23 |
| L11-8418 | Flooring at Elevator Lobby | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 3 |
| L12-8418 | Flooring at Elevator Lobby | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 3 |
| L05-7136 | Install Door and Hardware | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 22 |
| L07-7134 | Install VCT Flooring | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 17 |
| L09-7140 | Fire Alarm Trim (Install Devices) | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 3 |
| L10-7140 | Fire Alarm Trim (Install Devices) | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 3 |
| CO-7228 | Cx - Start-Up - Poolpak | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 37 |
| L10-8222 | Corridors - Fire Alarm Trim (Install Devices) | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 3 |
| L09-8222 | Corridors - Fire Alarm Trim (Install Devices) | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 3 |
| L09-8420 | Fire Alarm Trim (Install Devices) | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 3 |
| L10-8420 | Fire Alarm Trim (Install Devices) | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 3 |

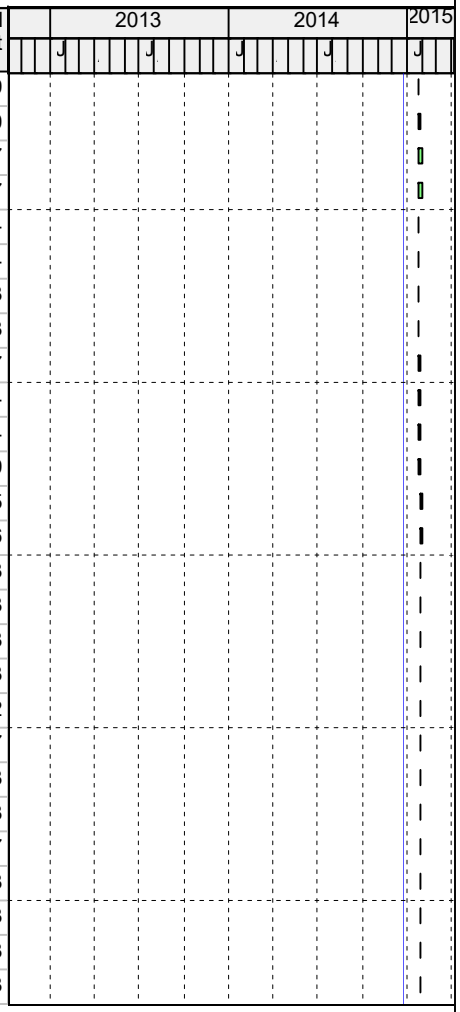



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 5 |
| L12-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 5 |
| L03-8618 | L3 Pool - Ceramic tile at pool area | 5 | 5 | 27-Jan-15 | 02-Feb-15 | 14 |
| L06-7136 | Install Door and Hardware | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 21 |
| L08-7134 | Install VCT Flooring | 2 | 2 | 27-Jan-15 | 28-Jan-15 | 17 |
| L05-7146 | Final Coat Finish Paint | 2 | 2 | 27-Jan-15 | 28-Jan-15 | 22 |
| SW-2216 | Zone 2 - Install irrigation | 5 | 5 | 27-Jan-15 | 02-Feb-15 | 41 |
| SW-2218 | Zone 2 - Install landscaping | 5 | 5 | 27-Jan-15 | 02-Feb-15 | 41 |
| CO-7224 | Cx - Start-Up - Gravity Relief Ventilator | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 12 |
| L1K-8128a | Kitchen Equipment Final Connections | 5 | 5 | 27-Jan-15 | 02-Feb-15 | 19 |
| CO-7248 | Cx - Heat Pump Start-Up - Levels 11 & 12 | 5 | 5 | 27-Jan-15 | 02-Feb-15 | 26 |
| CO-7136 | Cx - DDC Point-To-Point - MUA AAON Start-Up (8) | 5 | 5 | 27-Jan-15 | 02-Feb-15 | 29 |
| SW-2048 | Zone 4 - FRP Porte Cochere drive | 6 | 6 | 27-Jan-15 | 03-Feb-15 | 30 |
| CO-7140 | Fire Alarm System Device Testing - Tower Levels 4 thr | 4 | 4 | 27-Jan-15 | 30-Jan-15 | 3 |
| MPP-1042 | (C) Caulking - Pool deck | 5 | 5 | 27-Jan-15 | 02-Feb-15 | 20 |
| MPP-1044 | (C) Caulking - Elevation 9/10/11/12/13 (upper ballroor | 5 | 5 | 27-Jan-15 | 02-Feb-15 | 20 |
| L11-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 28-Jan-15 | 29-Jan-15 | 21 |
| L12-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 28-Jan-15 | 29-Jan-15 | 21 |
| L14-8418 | Flooring at Elevator Lobby | 2 | 2 | 28-Jan-15 | 29-Jan-15 | 3 |
| L15-8418 | Flooring at Elevator Lobby | 2 | 2 | 28-Jan-15 | 29-Jan-15 | 3 |
| LL1-Z2-8118a | Install decorative light fixtures | 3 | 3 | 28-Jan-15 | 30-Jan-15 | 20 |
| LL1-Z3-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 28-Jan-15* | 29-Jan-15 | 22 |
| L07-7136 | Install Door and Hardware | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 20 |
| L09-7134 | Install VCT Flooring | 2 | 2 | 28-Jan-15 | 29-Jan-15 | 17 |
| L11-7140 | Fire Alarm Trim (Install Devices) | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 7 |
| L12-7140 | Fire Alarm Trim (Install Devices) | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 7 |
| L03-8642 | L3 Pool - Fill pool | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 38 |

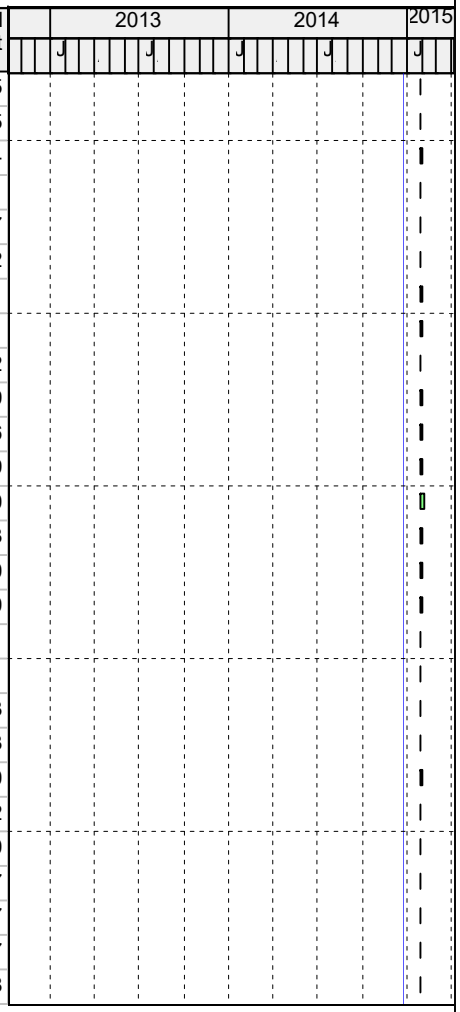



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7146 | Final Coat Finish Paint | 2 | 2 | 28-Jan-15 | 29-Jan-15 | 21 |
| CO-7230 | Cx - TAB - Air Balancing | 15 | 15 | 28-Jan-15 | 17-Feb-15 | 12 |
| L1K-8206 | Install Restroom Fixtures | 5 | 5 | 28-Jan-15 | 03-Feb-15 | 16 |
| L12-8222 | Corridors - Fire Alarm Trim (Install Devices) | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 5 |
| L11-8222 | Corridors - Fire Alarm Trim (Install Devices) | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 5 |
| L11-8420 | Fire Alarm Trim (Install Devices) | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 5 |
| L12-8420 | Fire Alarm Trim (Install Devices) | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 5 |
| L1BOH2-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 29-Jan-15 | 30-Jan-15 | 16 |
| L1BOH2-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 29-Jan-15 | 30-Jan-15 | 15 |
| L1BOH2-8204 | Mech Trim / Finish (HVAC & Plumbing) | 2 | 2 | 29-Jan-15 | 30-Jan-15 | 16 |
| L03-8418 | Flooring at Elevator Lobby | 2 | 2 | 29-Jan-15 | 30-Jan-15 | 4 |
| L14-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 29-Jan-15 | 29-Jan-15 | 4 |
| L14-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 29-Jan-15 | 30-Jan-15 | 20 |
| L15-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 29-Jan-15 | 29-Jan-15 | 4 |
| L08-7136 | Install Door and Hardware | 1 | 1 | 29-Jan-15 | 29-Jan-15 | 19 |
| L10-7134 | Install VCT Flooring | 2 | 2 | 29-Jan-15 | 30-Jan-15 | 21 |
| L11-7134 | Install VCT Flooring | 2 | 2 | 29-Jan-15 | 30-Jan-15 | 18 |
| L12-7134 | Install VCT Flooring | 2 | 2 | 29-Jan-15 | 30-Jan-15 | 18 |
| L07-7146 | Final Coat Finish Paint | 2 | 2 | 29-Jan-15 | 30-Jan-15 | 20 |
| L03-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 4 |
| L15-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 30-Jan-15 | 02-Feb-15 | 19 |
| L16-8418 | Flooring at Elevator Lobby | 2 | 2 | 30-Jan-15 | 02-Feb-15 | 3 |
| L17-8418 | Flooring at Elevator Lobby | 2 | 2 | 30-Jan-15 | 02-Feb-15 | 3 |
| L09-7136 | Install Door and Hardware | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 18 |
| L14-7140 | Fire Alarm Trim (Install Devices) | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 5 |
| L15-7140 | Fire Alarm Trim (Install Devices) | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 5 |
| L08-7146 | Final Coat Finish Paint | 2 | 2 | 30-Jan-15 | 02-Feb-15 | 19 |

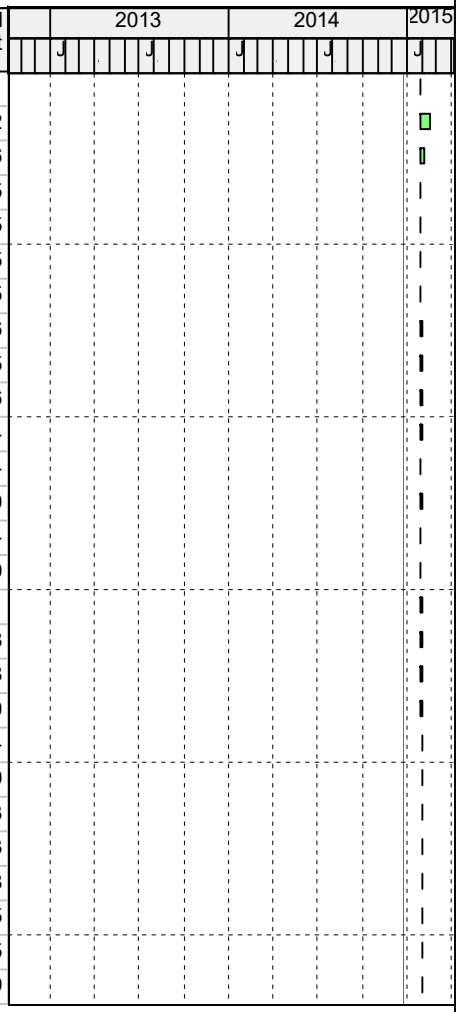



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8222 | Corridors - Fire Alarm Trim (Install Devices) | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 4 |
| L14-8222 | Corridors - Fire Alarm Trim (Install Devices) | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 4 |
| I-1206 | Concierge Lounge - Ceiling | 15 | 15 | 30-Jan-15 | 19-Feb-15 | 1 |
| L14-8420 | Fire Alarm Trim (Install Devices) | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 4 |
| L15-8420 | Fire Alarm Trim (Install Devices) | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 4 |
| L14-7134 | Install VCT Flooring | 2 | 2 | 31-Jan-15 | 02-Feb-15 | 18 |
| L15-7134 | Install VCT Flooring | 2 | 2 | 31-Jan-15 | 02-Feb-15 | 18 |
| L1BOH2-8201 | Final Coat Finish Paint | 5 | 5 | 02-Feb-15 | 06-Feb-15 | 16 |
| L03-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 02-Feb-15 | 03-Feb-15 | 17 |
| L16-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 3 |
| L17-8408 | Install Wood Base at Elevator Lobby | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 3 |
| CO-7110T | Fire Sprinkler Pre-Testing (Tower) - Tower Levels 4 thru | 6 | 6 | 02-Feb-15 | 09-Feb-15 | 3 |
| CO-7116T | Fire Alarm Pre-Testing (Tower) - Tower Levels 4 thru 1( | 6 | 6 | 02-Feb-15 | 09-Feb-15 | 3 |
| L03-7140 | Fire Alarm Trim (Install Devices) | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 4 |
| L10-7136 | Install Door and Hardware | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 17 |
| L11-7136 | Install Door and Hardware | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 17 |
| L12-7136 | Install Door and Hardware | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 17 |
| L1K-8124b | Install Base | 3 | 3 | 02-Feb-15 | 04-Feb-15 | 17 |
| L09-7146 | Final Coat Finish Paint | 2 | 2 | 02-Feb-15 | 03-Feb-15 | 18 |
| L03-8222 | Corridors - Fire Alarm Trim (Install Devices) | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 4 |
| L1K-8142 | MEP Trim | 5 | 5 | 02-Feb-15 | 06-Feb-15 | 10 |
| L03-8420 | Fire Alarm Trim (Install Devices) | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 4 |
| L16-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 17 |
| L17-8412 | Final Coat Finish Paint at Elevator Lobby | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 17 |
| L03-8620 | L3 Pool - Plumbing Fixtures & Trim / Finish | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 14 |
| L03-8626 | L3 Pool - Elec Trim/ Finish | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 14 |
| L03-8628 | L3 Pool - Elec Specialties Trim / Finish | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 14 |

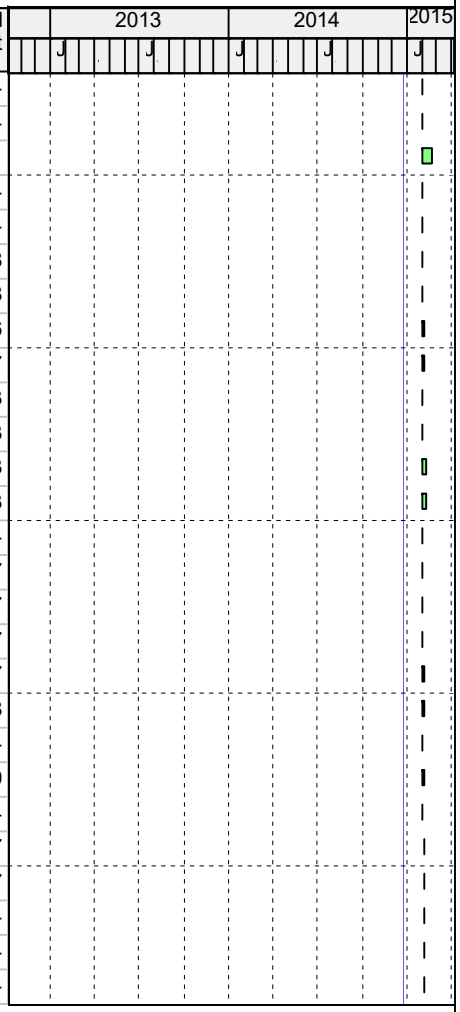



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8630 | L3 Pool - Doors & Hardware | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 14 |
| L03-7134 | Install VCT Flooring & Base | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 12 |
| L14-7136 | Install Door and Hardware | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 16 |
| L15-7136 | Install Door and Hardware | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 16 |
| L16-7140 | Fire Alarm Trim (Install Devices) | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 3 |
| L17-7140 | Fire Alarm Trim (Install Devices) | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 3 |
| L03-8638 | L3 Pool - Install pool deck and ADA lift | 3 | 3 | 03-Feb-15 | 05-Feb-15 | 32 |
| L10-7146 | Final Coat Finish Paint | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 17 |
| L11-7146 | Final Coat Finish Paint | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 17 |
| L12-7146 | Final Coat Finish Paint | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 17 |
| RF-4066 | Pool Green Roof - Install decorative metal railing | 3 | 3 | 03-Feb-15 | 05-Feb-15 | 30 |
| MPP-1014 | (A) Caulking - Elevation 1/2/A/B/C/23/24/25 (west ele | 9 | 9 | 03-Feb-15 | 13-Feb-15 | 17 |
| L17-8222 | Corridors - Fire Alarm Trim (Install Devices) | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 3 |
| L16-8222 | Corridors - Fire Alarm Trim (Install Devices) | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 3 |
| CO-7250 | Cx - Heat Pump Start-Up - Levels 14 & 15 | 5 | 5 | 03-Feb-15 | 09-Feb-15 | 26 |
| CO-7402 | Cx - FPT - Central Plant | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 29 |
| CO-7404 | Cx - FPT - Heat Pumps | 3 | 3 | 03-Feb-15 | 05-Feb-15 | 33 |
| MPT-1094 | (C) Caulking - Elevation 32 (south elevation, east of n | 10 | 10 | 03-Feb-15 | 16-Feb-15 | 20 |
| MPT-1096 | (B) Caulking - Elevation 33/34 (east elevation, south e | 10 | 10 | 03-Feb-15 | 16-Feb-15 | 26 |
| L16-8420 | Fire Alarm Trim (Install Devices) | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 3 |
| L17-8420 | Fire Alarm Trim (Install Devices) | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 3 |
| L16-7134 | Install VCT Flooring | 2 | 2 | 04-Feb-15 | 05-Feb-15 | 17 |
| L17-7134 | Install VCT Flooring | 2 | 2 | 04-Feb-15 | 05-Feb-15 | 17 |
| L14-7146 | Final Coat Finish Paint | 2 | 2 | 04-Feb-15 | 05-Feb-15 | 16 |
| L15-7146 | Final Coat Finish Paint | 2 | 2 | 04-Feb-15 | 05-Feb-15 | 16 |
| L1K-8208 | Install Restroom Accessories | 2 | 2 | 04-Feb-15 | 05-Feb-15 | 16 |
| CO-7140.1 | Fire Alarm System Device Testing - Tower Levels 3, 1 | 4 | 4 | 04-Feb-15 | 09-Feb-15 | 3 |

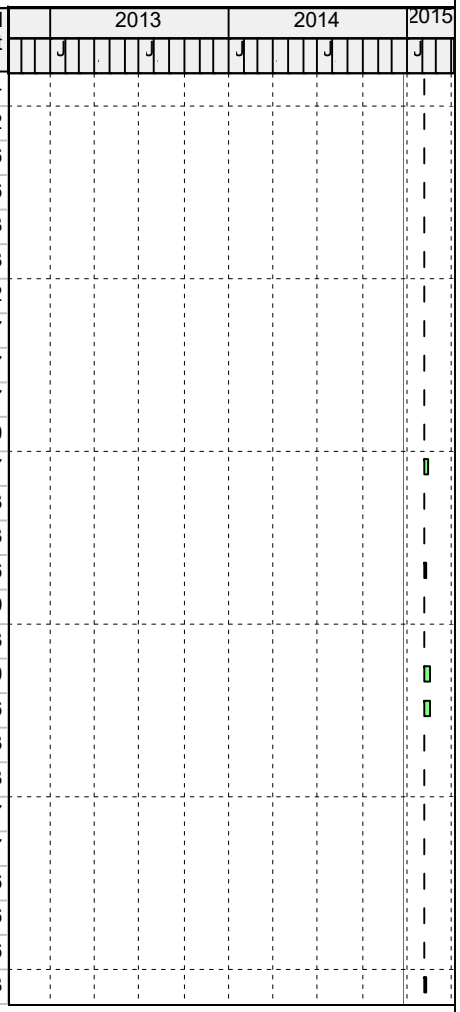



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-8120 | Install operable partitions | 3 | 3 | 05-Feb-15 | 09-Feb-15 | 10 |
| L03-8632 | L3 Pool - Install Bathroom Accessories | 2 | 2 | 05-Feb-15 | 06-Feb-15 | 14 |
| L03-7136 | Install Doors and Hardware | 2 | 2 | 05-Feb-15 | 06-Feb-15 | 12 |
| L1B-8128 | Install Base | 2 | 2 | 05-Feb-15 | 06-Feb-15 | 11 |
| CO-7408 | Cx - FPT - Garage Exhaust Fans | 1 | 1 | 05-Feb-15 | 05-Feb-15 | 29 |
| L16-7136 | Install Door and Hardware | 1 | 1 | 06-Feb-15 | 06-Feb-15 | 14 |
| L17-7136 | Install Door and Hardware | 1 | 1 | 06-Feb-15 | 06-Feb-15 | 14 |
| L16-7146 | Final Coat Finish Paint | 2 | 2 | 06-Feb-15 | 09-Feb-15 | 14 |
| L17-7146 | Final Coat Finish Paint | 2 | 2 | 06-Feb-15 | 09-Feb-15 | 14 |
| RF-4068 | Pool Green Roof - Install American Hydrotech assemI | 3 | 3 | 06-Feb-15 | 10-Feb-15 | 30 |
| CO-7410 | Cx - FPT - Misc Equipment | 4 | 4 | 06-Feb-15 | 11-Feb-15 | 29 |
| L1BOH2-8134 | Clean | 4 | 4 | 09-Feb-15 | 12-Feb-15 | 16 |
| L1BOH2-8132 | Punch | 4 | 4 | 09-Feb-15 | 12-Feb-15 | 16 |
| L03-8646 | L3 Pool - Health inspections | 1 | 1 | 09-Feb-15 | 09-Feb-15 | 31 |
| L03-7146 | Final Coat Finish Paint | 2 | 2 | 09-Feb-15 | 10-Feb-15 | 12 |
| MPP-1036 | Podium Signs, East | 5 | 5 | 09-Feb-15 | 13-Feb-15 | 22 |
| CO-7104T | Fire Alarm & Smoke Control Pre-Testing (Tower) - Tow | 7 | 7 | 10-Feb-15 | 18-Feb-15 | 9 |
| CO-7218 | Cx - Heat Pump Start-Up - Levels 16 & 17 | 5 | 5 | 10-Feb-15 | 16-Feb-15 | 26 |
| CO-7110T.1 | Fire Sprinkler Pre-Testing (Tower) - Tower Levels 11 thi | 6 | 6 | 10-Feb-15 | 17-Feb-15 | 3 |
| O-7116T.1 | Fire Alarm Pre-Testing (Tower) - Tower Levels 11 thru | 6 | 6 | 10-Feb-15 | 17-Feb-15 | 3 |
| MPT-1092 | (C) Caulking - Elevation 31 (above L12 terrace, west | 4 | 4 | 11-Feb-15 | 16-Feb-15 | 20 |
| CM-1024 | Tower - "Clean/Punch" Complete - All Floors | 0 | 0 | | 11-Feb-15 | 34 |
| L1BOH2-81214 | L1, Zone 3 Complete | 0 | 0 | | 12-Feb-15 | 16 |
| CM-1016a | CM - Owner FF+E "Build-Out" - Floors 3, 11-17 | 17 | 17 | 16-Feb-15 | 04-Mar-15 | 16 |
| CO-7406 | Cx - FPT - MUA, RTU, VAV and Exhaust Fans | 5 | 5 | 16-Feb-15 | 20-Feb-15 | 12 |
| MPP-1048 | (A) Caulking - Porte Cochere cornice metal | 3 | 3 | 16-Feb-15 | 18-Feb-15 | 17 |
| CO-7104T.1 | Fire Alarm & Smoke Control Pre-Testing (Tower) - Tow | 7 | 7 | 18-Feb-15 | 26-Feb-15 | 3 |

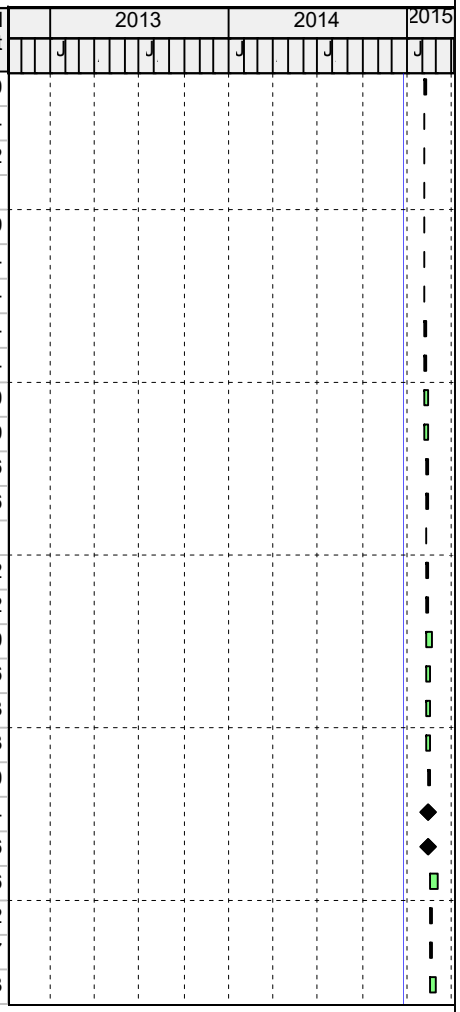



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1204 | Concierge Lounge - Additional millwork | 4 | 4 | 19-Feb-15 | 24-Feb-15 | 4 |
| CO-7142 | Fire Alarm System Device Testing - Podium | 7 | 7 | 19-Feb-15 | 27-Feb-15 | 2 |
| MPT-1098 | (A) Caulking - Elevation 3/30 (south elevation, west of | 6 | 6 | 19-Feb-15 | 26-Feb-15 | 17 |
| RF-4070 | TR - Terrace Roof - Install American Hydrotech assem | 3 | 3 | 20-Feb-15 | 24-Feb-15 | 20 |
| I-1202 | Concierge Lounge - Additional flooring work | 3 | 3 | 23-Feb-15 | 25-Feb-15 | 0 |
| L1L-8120 | Install plumbing at bar | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 1 |
| L1L-8122 | Install electrical at bar | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 1 |
| L1L-8124a | Install Base | 3 | 3 | 23-Feb-15 | 25-Feb-15 | 0 |
| MPP-1038 | Podium Signs, West | 5 | 5 | 23-Feb-15 | 27-Feb-15 | 17 |
| MPT-1074 | Tower Sign, South (El 32) | 5 | 5 | 23-Feb-15 | 27-Feb-15 | 17 |
| CO-7138 | Elevator Finals with AHJ | 10 | 10 | 27-Feb-15 | 12-Mar-15 | 3 |
| CO-7112T | City of Bellevue/3rd Party Fire Sprinkler Inspection / A | 6 | 6 | 05-Mar-15 | 12-Mar-15 | 3 |
| CO-7118T | City of Bellevue/3rd Party Fire Alarm Inspection / Appl | 6 | 6 | 05-Mar-15 | 12-Mar-15 | 3 |
| CO-7106T | City of Bellevue/3rd Party Smoke Control Testing (Tow | 6 | 6 | 05-Mar-15 | 12-Mar-15 | 3 |
| CM-1022 | Podium - "Clean/Punch" Complete - All Floors, All Zon | 0 | 0 | | 06-Mar-15 | 17 |
| CO-7412 | Cx - Pressure Testing - GC Indicates Building Comple | 0 | 0 | | 06-Mar-15 | 0 |
| CO-7416 | Cx - Pressure Testing - Pre-Walk with GC | 1 | 1 | 09-Mar-15 | 09-Mar-15 | 0 |
| CO-7418 | Cx - Pressure Testing - GC Makes Corrections | 5 | 5 | 09-Mar-15 | 13-Mar-15 | 0 |
| CO-7420 | Cx - Pressure Testing - Pressure Pre-Test | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 0 |
| CO-7422 | Cx - Pressure Testing -Corrections | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 0 |
| CO-7424 | Cx - Pressure Testing - Pressure Final Test | 1 | 1 | 20-Mar-15 | 20-Mar-15 | 0 |
| CO-7426 | Cx - Pressure Testing - Building Final Corrections | 2 | 2 | 23-Mar-15 | 24-Mar-15 | 0 |
| CO-7124 | Complete Final Building Inspections | 5 | 5 | 25-Mar-15 | 31-Mar-15 | 0 |
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13 A | | |

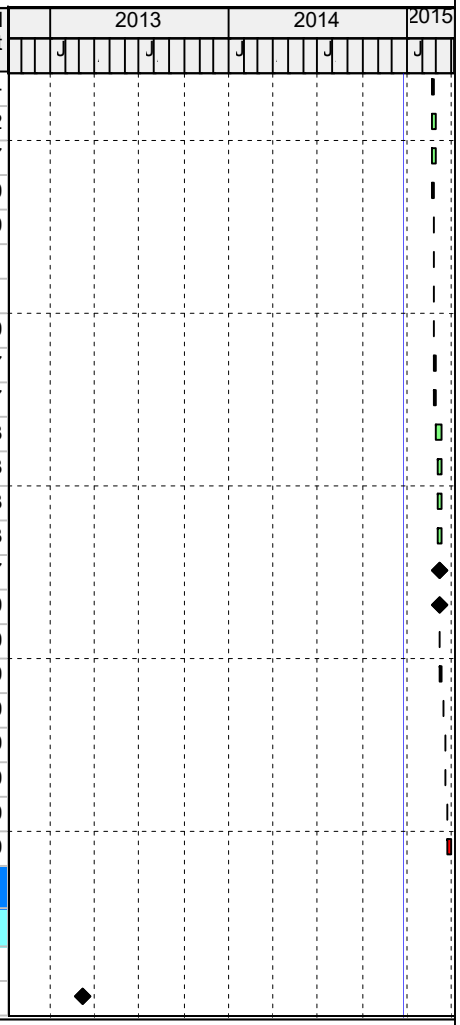



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CM-1002 | CM - Contract Time (578 Cal Days) | 576 | 0 | 06-Mar-13 A | 05-Oct-14 A | |
| CM-1014 | CM - Start of Construction | 0 | 0 | 05-Apr-13 A | | |
| CM-1006 | Construction Documents Issued by Client - (Due on 7 | 0 | 0 | 22-Dec-14 | | 100 |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 22-Dec-14* | | 51 |
| CO-7004 | CO - Prep / Submit O&M Manuals | 40 | 40 | 22-Dec-14 | 30-Jan-15 | 60 |
| CM-1008 | Finalization of Allowances - (Due on 9-2-13) | 0 | 0 | 22-Dec-14 | | 100 |
| CM-1016 | CM - Owner FF+E "Build-Out" - Floors 4-10 | 21 | 21 | 26-Jan-15* | 15-Feb-15 | 16 |
| CM-1018 | CM - Hotel Operations Training | 21 | 21 | 23-Feb-15 | 15-Mar-15 | 16 |
| CO-7006 | CO - Certificate of Occupancy/Substantial Completior | 0 | 0 | | 31-Mar-15 | 0 |
| CO-7122 | CO - Certificate of Occupancy | 0 | 0 | | 31-Mar-15 | 0 |
| **Misc Milestones** | | | | | | |
| CM-1020 | MM - Site Mobilization | 10 | 0 | 06-Mar-13 A | 04-Apr-13 A | |
| MM-1008 | MM - Top Out - Tower / Structure | 0 | 0 | | 16-Apr-14 A | |
| MM-1004 | MM - Start Drywall In Tower | 0 | 0 | 27-Jun-14 A | | |
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 06-Sep-14 A | |
| MM-1010 | Energize Permanent Power | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| **Tower Crane** | | | | | | |
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 0 | 04-Jun-13 A | 14-Jun-13 A | |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 0 | 20-Jun-13 A | 24-Jun-13 A | |
| TC-5902 | Tower Crane - Erectiion | 2 | 0 | 21-Jun-13 A | 24-Jun-13 A | |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 24-Jun-13 A | | |
| TC-5906 | Tower Crane - Operatational Period | 391 | 0 | 24-Jun-13 A | 16-Jun-14 A | |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 0 | 16-Jun-14 A | 17-Jun-14 A | |
| **Man & Material Lifts** | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 0 | 14-Jan-14 A | 20-Jan-14 A | |
| ML-5952 | Man/Material Lifts - Erect/Build Loading Dock | 5 | 0 | 21-Jan-14 A | 27-Jan-14 A | |

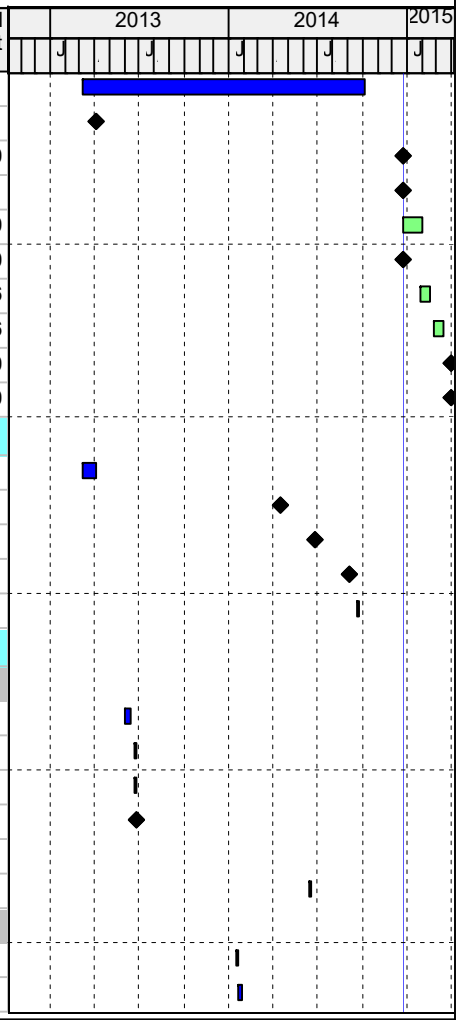


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 10-Feb-14 A | | |
| ML-5954 | Man/Material Lifts - Load Test / Certify | 1 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| ML-5958 | Man/Material Lifts - Operatational Period | 196 | 0 | 10-Feb-14 A | 15-Nov-14 A | |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 2 | 0 | 15-Nov-14 A | 16-Nov-14 A | |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |
| **Mass Excavation / Shoring** | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 0 | 05-Apr-13 A | 12-Apr-13 A | |
| SW-2002 | Demolition And Utility Relocation | 8 | 0 | 15-Apr-13 A | 19-Apr-13 A | |
| SW-2010 | Grade Subgrade for Elect/Plumbing | 3 | 0 | 07-Jan-14 A | 09-Jan-14 A | |
| **Site Finishes** | | | | | | |
| SW-2006 | Install Perm Power Electrical Service / Dry Utilities (Off | 15 | 0 | 20-May-14 A | 05-Jun-14 A | |
| SW-2004 | Offsite Water & Water Connection | 9 | 0 | 22-Sep-14 A | 01-Oct-14 A | |
| SW-2008 | Zone 4 - Landscaping & irrigation | 5 | 5 | 04-Feb-15 | 10-Feb-15 | 30 |
| **Structure** | | | | | | |
| **Foundation / Substructure - (Levels LL4 / LL3)** | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 0 | 12-Jun-13 A | 27-Jun-13 A | |
| LL4-1601 | LL4 - Excavate Footings | 14 | 0 | 17-Jun-13 A | 30-Jul-13 A | |
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 0 | 18-Jun-13 A | 24-Jun-13 A | |
| LL4-1606 | LL4 - Undrgmd Plumbing | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-1608 | LL4 - Undrgmd Elec | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 0 | 19-Jun-13 A | 25-Jun-13 A | |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 0 | 26-Jun-13 A | 02-Aug-13 A | |
| LL4-2033 | LL4 - Shotcrete Walls | 27 | 0 | 26-Jun-13 A | 05-Aug-13 A | |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 0 | 03-Jul-13 A | 21-Aug-13 A | |

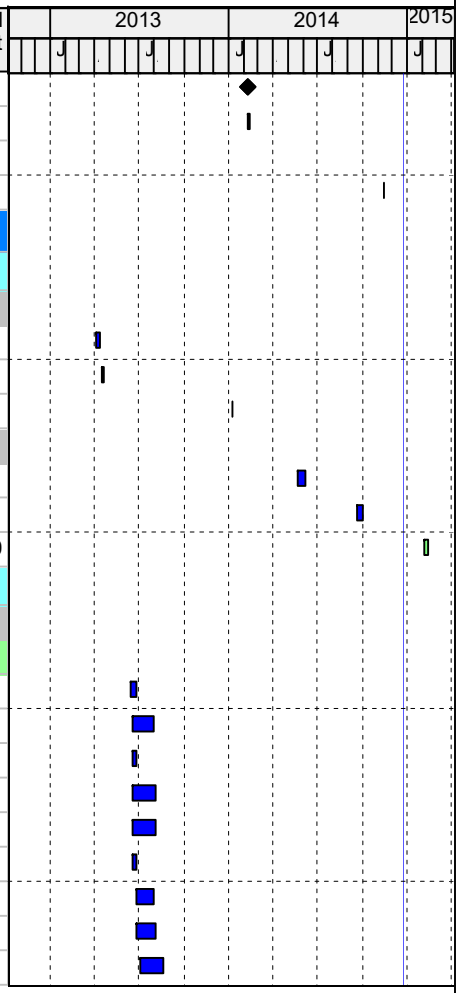



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-1614 | LL4 - FRP SOG | 5 | 0 | 10-Jul-13 A | 07-Aug-13 A | |
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 0 | 12-Jul-13 A | 26-Jul-13 A | |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 0 | 13-Jul-13 A | 06-Aug-13 A | |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 0 | 22-Jul-13 A | 24-Jul-13 A | |
| LL4-1618 | LL4 - FRP Ramp SOG | 5 | 0 | 01-Aug-13 A | 07-Aug-13 A | |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2004 | LL2 - Shore / Form Deck | 8 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2006 | LL3 - M & E Inserts | 4 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2008 | LL3 - ReSteel / PT Cables | 6 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2010 | LL3 - Install Embeds | 2 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2001 | LL3 - Waterproof Walls | 3 | 0 | 05-Aug-13 A | 05-Aug-13 A | |
| LL3-2012 | LL3 - Pour / Finish Deck | 2 | 0 | 16-Aug-13 A | 16-Aug-13 A | |
| LL3-2014 | LL3 - Stress Tendons | 1 | 0 | 19-Aug-13 A | 19-Aug-13 A | |
| LL3-2000 | LL3 - FRP Core Walls | 8 | 0 | 19-Aug-13 A | 28-Aug-13 A | |
| LL3-2033 | LL3 - Shotcrete Walls | 5 | 0 | 23-Aug-13 A | 26-Aug-13 A | |
| LL3-2016 | LL3 - Strip / ReShore Deck | 3 | 0 | 01-Sep-13 A | 13-Sep-13 A | |
| LL3-2018 | LL3 - Remove ReShores | 4 | 0 | 04-Nov-13 A | 07-Nov-13 A | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Grids 1 to 4 - (SOG @ Loading Dock)** | | | | | | |
| LL2-2056 | LL2 - Grease Intercepter | 5 | 0 | 15-Aug-13 A | 21-Aug-13 A | |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 0 | 27-Aug-13 A | 04-Sep-13 A | |
| LL2-2027 | LL2 - Waterproof Walls | 2 | 0 | 27-Aug-13 A | 28-Aug-13 A | |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 0 | 30-Aug-13 A | 05-Sep-13 A | |
| LL2-2021 | LL2 - FRP Elec Vault | 14 | 0 | 30-Aug-13 A | 04-Sep-13 A | |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 0 | 04-Sep-13 A | 11-Sep-13 A | |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 0 | 11-Sep-13 A | 13-Sep-13 A | |

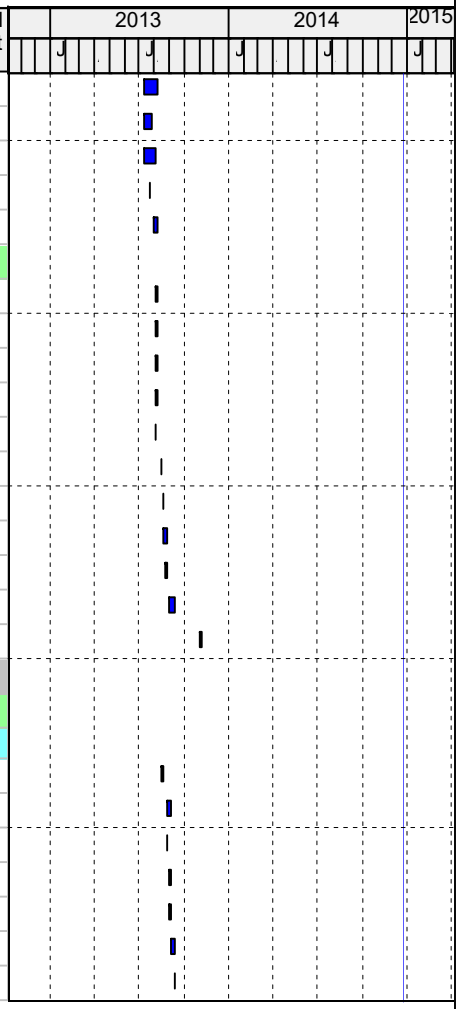



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls/Roof | 11 | 0 | 19-Sep-13 A | 03-Oct-13 A | |
| LL2-2020 | LL2 - Undrgmd Plumbing | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2022 | LL2 - Undrgmd Elec | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2031 | LL2 - FRP Generator SOG | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2015 | LL2 to LL1 FRP Columns / Misc Walls | 6 | 0 | 01-Oct-13 A | 01-Oct-13 A | |
| LL2-2029 | LL2 - F/R/P Pour #2 | 8 | 0 | 15-Jan-14 A | 24-Jan-14 A | |
| LL2-2011 | LL2 - F/R/P Pour #3 | 16 | 0 | 24-Jan-14 A | 18-Feb-14 A | |
| LL2-2019 | LL2 - F/R/P Pour #6 | 4 | 0 | 19-Feb-14 A | 17-Mar-14 A | |
| LL2-2044 | LL2 - Set Generator | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |
| LL2-2004 | LL2 - Shore / Form Deck | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2035 | LL2 to LL1 - Shotcrete Walls | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2006 | LL2 - M & E Inserts | 4 | 0 | 14-Aug-13 A | 19-Aug-13 A | |
| LL2-2008 | LL2 - ReSteel / PT Cables | 6 | 0 | 14-Aug-13 A | 21-Aug-13 A | |
| LL2-2010 | LL2 - Install Embeds | 3 | 0 | 14-Aug-13 A | 16-Aug-13 A | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 0 | 27-Aug-13 A | 06-Sep-13 A | |
| LL2-2012 | LL2 - Place / Finish Deck | 3 | 0 | 29-Aug-13 A | 29-Aug-13 A | |
| LL2-2023 | LL2 - Waterproof Walls | 3 | 0 | 29-Aug-13 A | 03-Sep-13 A | |
| LL2-2014 | LL2 - Stress Tendons | 1 | 0 | 30-Aug-13 A | 30-Aug-13 A | |
| LL2-2016 | LL2 - Strip / ReShore | 3 | 0 | 03-Sep-13 A | 05-Sep-13 A | |
| LL2-8234 | LL2 - Place / Finish Deck | 3 | 0 | 12-Sep-13 A | 12-Sep-13 A | |
| LL2-2000 | LL2 - FRP Core Walls | 8 | 0 | 12-Sep-13 A | 23-Sep-13 A | |
| LL2-2018 | LL2 - Remove ReShores | 4 | 0 | 13-Nov-13 A | 18-Nov-13 A | |
| LL2-2013 | LL2 - F/R/P Pour #1 | 4 | 0 | 13-Jan-14 A | 16-Jan-14 A | |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| P5A-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |

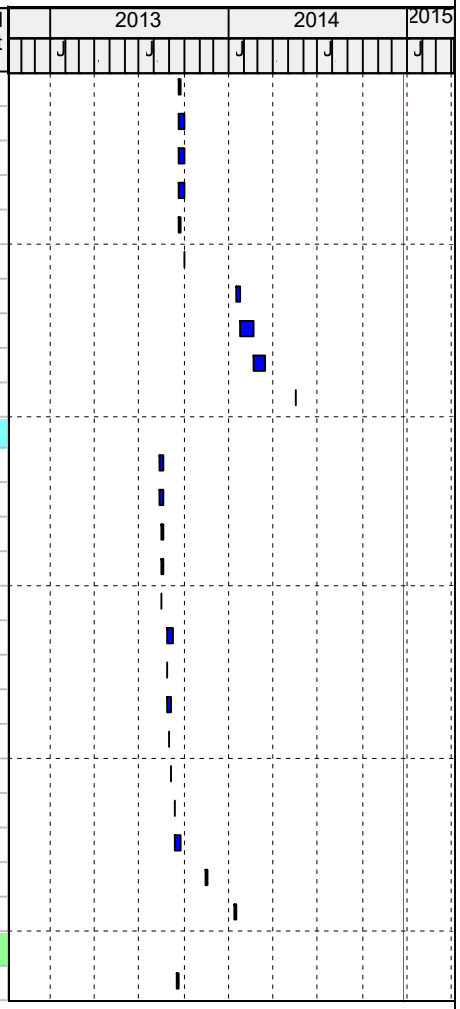


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P5A-2000 | LL1 - FRP Core Walls | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2004 | LL1 - Shore / Form Deck | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| P6-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P6-2004 | LL1 - Shore / Form Deck | 7 | 0 | 16-Sep-13 A | 24-Sep-13 A | |
| P5A-2006 | LL1 - MEP Rough In | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2008 | LL1 - ReSteel / PT Cables | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2012 | LL1 - Place / Finish Deck | 0 | 0 | 20-Sep-13 A | | |
| P5A-2020 | LL1 - Waterproof Walls | 3 | 0 | 20-Sep-13 A | 24-Sep-13 A | |
| P5A-2014 | LL1 - Stress Tendons | 1 | 0 | 23-Sep-13 A | 23-Sep-13 A | |
| P5A-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2006 | LL1 - MEP Rough In | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2008 | LL1 - ReSteel / PT Cables | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 24-Sep-13 A | 25-Sep-13 A | |
| P6-2020 | LL1 - Waterproof Walls | 4 | 0 | 24-Sep-13 A | 27-Sep-13 A | |
| P5A-2033 | LL1 - Resteel/Shotcrete Walls | 3 | 0 | 25-Sep-13 A | 27-Sep-13 A | |
| P5B-2002 | LL1 - FRP Columns Below | 5 | 0 | 26-Sep-13 A | 02-Oct-13 A | |
| P5B-2004 | LL1 - Shore / Form Deck | 7 | 0 | 26-Sep-13 A | 04-Oct-13 A | |
| P6-2012 | LL1 - Place / Finish Deck | 0 | 0 | 27-Sep-13 A | | |
| P6-2014 | LL1 - Stress Tendons | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2033 | LL1 - Resteel/Shotcrete Walls | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 01-Oct-13 A | 03-Oct-13 A | |
| P5B-2006 | LL1 - MEP Rough In | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2002 | FRP Columns Below | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2004 | Shore / Form Deck | 4 | 0 | 03-Oct-13 A | 08-Oct-13 A | |
| P5B-2008 | LL1 - ReSteel / PT Cables | 5 | 0 | 04-Oct-13 A | 10-Oct-13 A | |
| P5B-2010 | LL1 - Install Edgeform/Embeds | 4 | 0 | 04-Oct-13 A | 09-Oct-13 A | |

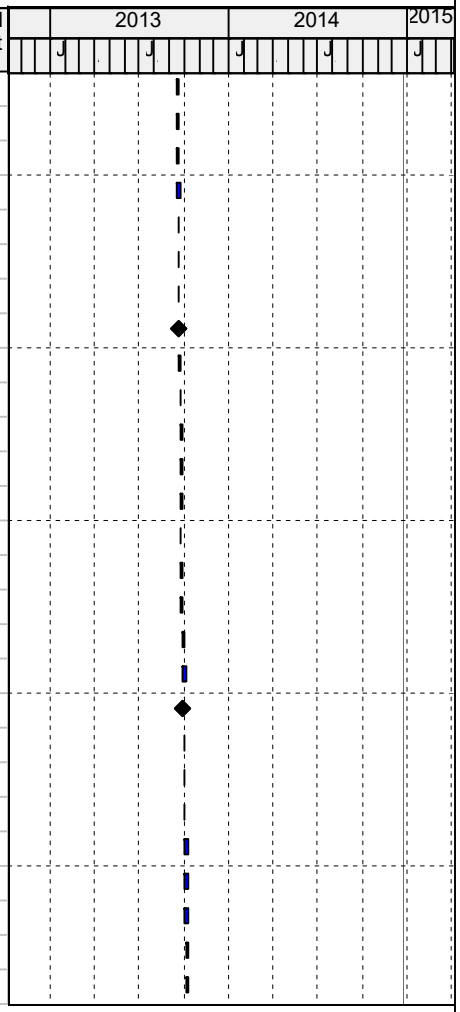


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P8-2002 | FRP Columns Below | 5 | 0 | 07-Oct-13 A | 11-Oct-13 A | |
| P8-2000 | Form/Resteel/Close Core Walls | 14 | 0 | 07-Oct-13 A | 24-Oct-13 A | |
| P8-2004 | Shore / Form Deck P8 | 8 | 0 | 07-Oct-13 A | 16-Oct-13 A | |
| P7-2002 | FRP Columns Below | 5 | 0 | 08-Oct-13 A | 14-Oct-13 A | |
| P7-2004 | Shore / Form Deck | 6 | 0 | 08-Oct-13 A | 15-Oct-13 A | |
| P10A--2006 | MEP Rough In | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2008 | ReSteel / PT Cables | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2010 | Install Edgeform/Embeds | 2 | 0 | 08-Oct-13 A | 09-Oct-13 A | |
| P5B-2012 | LL1 - Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P10A--2012 | Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P5B-2014 | LL1 - Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P7-2006 | MEP Rough In | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P7-2008 | ReSteel / PT Cables | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P10A--2014 | Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P8-2020 | Shore / Form Deck P9 | 6 | 0 | 14-Oct-13 A | 21-Oct-13 A | |
| P5B-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2010 | Install Edgeform/Embeds | 2 | 0 | 15-Oct-13 A | 16-Oct-13 A | |
| P8-2006 | MEP Rough In | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2008 | ReSteel / PT Cables | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2010 | Install Edgeform/Embeds | 4 | 0 | 15-Oct-13 A | 18-Oct-13 A | |
| P10A--2016 | Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2012 | Place / Finish Deck | 0 | 0 | 18-Oct-13 A | | |
| P7-2033 | Resteel/Shotcrete Walls | 3 | 0 | 18-Oct-13 A | 22-Oct-13 A | |
| P7-2014 | Stress Tendons | 1 | 0 | 21-Oct-13 A | 21-Oct-13 A | |
| P7-2016 | Strip / ReShore Deck | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2002 | FRP Columns Below | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P10B--2000 | FRP Shear Walls Below | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |

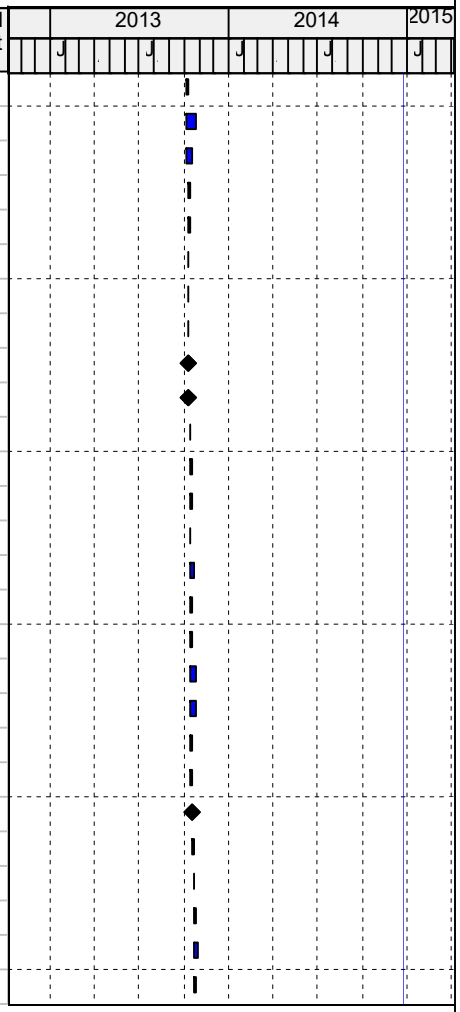


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P10B--2004 | Shore / Form Deck | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P8-2012 | Place / Finish Deck P 8 & 9 and Core Walls | 0 | 0 | 25-Oct-13 A | | |
| P8-2014 | Stress Tendons | 1 | 0 | 28-Oct-13 A | 28-Oct-13 A | |
| P10B--2006 | MEP Rough In | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2008 | ReSteel / PT Cables | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2010 | Install Edgeform/Embeds | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P12--2002 | FRP Columns Below | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P12--2000 | Form/Resteel/Close Core Walls | 9 | 0 | 28-Oct-13 A | 07-Nov-13 A | |
| P12--2004 | Shore / Form Deck | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P8-2016 | Strip / ReShore Deck | 3 | 0 | 29-Oct-13 A | 31-Oct-13 A | |
| P11--2002 | FRP Columns Below | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P11--2004 | Shore / Form Deck | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P10B--2012 | Place / Finish Deck | 0 | 0 | 31-Oct-13 A | | |
| P10B--2014 | Stress Tendons | 1 | 0 | 01-Nov-13 A | 01-Nov-13 A | |
| P12--2006 | MEP Rough In | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12--2008 | ReSteel / PT Cables | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12--2010 | Install Edgeform/Embeds | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P10B--2016 | Strip / ReShore Deck | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2006 | MEP Rough In | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2008 | ReSteel / PT Cables | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2010 | Install Edgeform/Embeds | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2012 | Place / Finish Deck | 0 | 0 | 07-Nov-13 A | | |
| P13--2002 | FRP Columns Below | 5 | 0 | 07-Nov-13 A | 14-Nov-13 A | |
| P13--2004 | Shore / Form Deck | 9 | 0 | 07-Nov-13 A | 28-Nov-13 A | |
| P11--2014 | Stress Tendons | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| P12--2012 | Place / Finish Deck & Core Walls | 0 | 0 | 08-Nov-13 A | | |
| P11--2016 | Strip / ReShore Deck | 3 | 0 | 12-Nov-13 A | 14-Nov-13 A | |

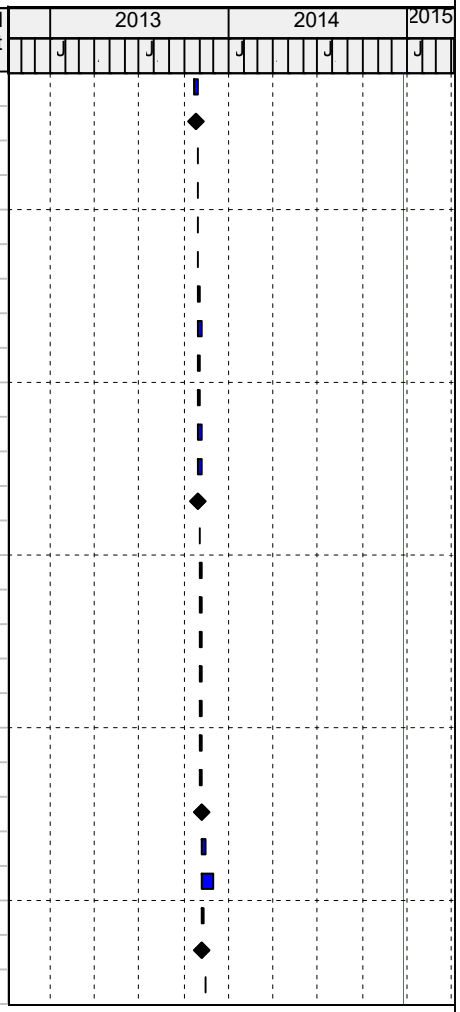


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P12–2014 | Stress Tendons | 1 | 0 | 12-Nov-13 A | 12-Nov-13 A | |
| P14–2002 | FRP Columns Below | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P14–2000 | Form/Resteel/Close Core Walls | 8 | 0 | 19-Nov-13 A | 03-Dec-13 A | |
| P14–2004 | Shore / Form Deck | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P13A–2002 | FRP Columns Below | 5 | 0 | 21-Nov-13 A | 27-Nov-13 A | |
| P13A–2004 | Shore / Form Deck | 4 | 0 | 21-Nov-13 A | 26-Nov-13 A | |
| P13–2010 | Install Edgeform/Embeds | 5 | 0 | 22-Nov-13 A | 04-Dec-13 A | |
| P13–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2006 | MEP Rough In | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2010 | Install Edgeform/Embeds | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P13–2006 | MEP Rough In | 5 | 0 | 26-Nov-13 A | 03-Dec-13 A | |
| P13A–2006 | MEP Rough In | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2008 | ReSteel / PT Cables | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2010 | Install Edgeform/Embeds | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13–2012 | Place / Finish Deck | 0 | 0 | 02-Dec-13 A | | |
| P13A–2012 | Place / Finish Deck | 0 | 0 | 03-Dec-13 A | | |
| P14–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 04-Dec-13 A | | |
| P13–2014 | Stress Tendons | 1 | 0 | 05-Dec-13 A | 05-Dec-13 A | |
| P15–2002 | FRP Columns Below | 3 | 0 | 05-Dec-13 A | 09-Dec-13 A | |
| P15–2000 | Jump/Resteel/Close Core | 9 | 0 | 05-Dec-13 A | 17-Dec-13 A | |
| P15–2004 | Shore / Form Deck | 5 | 0 | 05-Dec-13 A | 11-Dec-13 A | |
| P13–2016 | Strip / ReShore Deck | 3 | 0 | 06-Dec-13 A | 10-Dec-13 A | |
| P13A–2014 | Stress Tendons | 1 | 0 | 06-Dec-13 A | 06-Dec-13 A | |
| P14–2014 | Stress Tendons | 1 | 0 | 07-Dec-13 A | 07-Dec-13 A | |
| P15–2006 | MEP Rough In | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2008 | ReSteel / PT Cables | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |

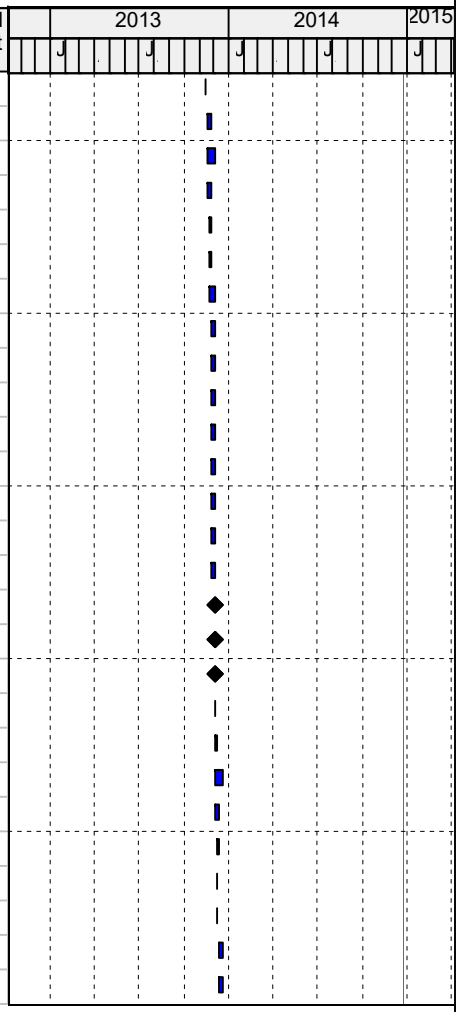


Actual Work | Critical Remai... | Remaining Work | Milestone | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P15–2010 | Install Edgeform/Embeds | 3 | 0 | 11-Dec-13 A | 13-Dec-13 A | |
| P16-2002 | FRP Columns Below | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P16-2004 | Shore / Form Deck | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P15–2012 | Place / Finish Deck | 0 | 0 | 18-Dec-13 A | | |
| P15–2020 | Place Conc @ Core | 0 | 0 | 18-Dec-13 A | | |
| P16-2000 | Jump/Resteel/Close Core | 5 | 0 | 18-Dec-13 A | 24-Dec-13 A | |
| P16-2006 | MEP Rough In | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2008 | ReSteel / PT Cables | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2010 | Install Edgeform/Embeds | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P15–2014 | Stress Tendons | 1 | 0 | 21-Dec-13 A | 21-Dec-13 A | |
| P8-2018 | Remove Reshores | 2 | 0 | 23-Dec-13 A | 24-Dec-13 A | |
| P10A–2018 | Remove Reshores | 2 | 0 | 26-Dec-13 A | 27-Dec-13 A | |
| P16-2012 | Place / Finish Deck | 0 | 0 | 26-Dec-13 A | | |
| P16-2020 | Place Conc @ Core | 0 | 0 | 26-Dec-13 A | | |
| P17-2002 | FRP Columns Below | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P17-2000 | Jump/Resteel/Close Core | 7 | 0 | 27-Dec-13 A | 07-Jan-14 A | |
| P17-2004 | Shore / Form Deck | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P10B–2018 | Remove Reshores | 2 | 0 | 30-Dec-13 A | 31-Dec-13 A | |
| P16-2014 | Stress Tendons | 1 | 0 | 31-Dec-13 A | 31-Dec-13 A | |
| P5A-2018 | LL1 - Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P11–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P12–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P17-2006 | MEP Rough In | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2008 | ReSteel / PT Cables | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2010 | Install Edgeform/Embeds | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P6-2018 | LL1 - Remove Reshores | 2 | 0 | 06-Jan-14 A | 07-Jan-14 A | |
| P5B-2018 | LL1 - Remove Reshores | 2 | 0 | 08-Jan-14 A | 09-Jan-14 A | |

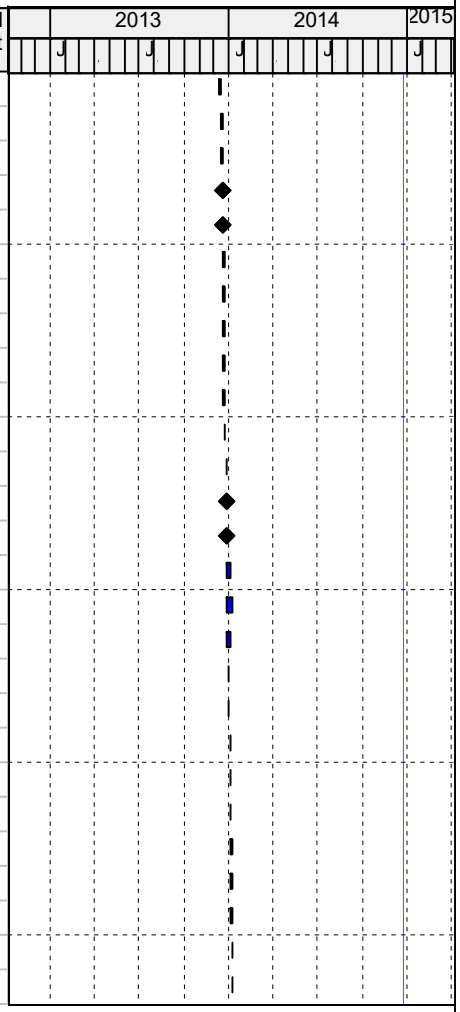


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P17-2012 | Place / Finish Deck | 0 | 0 | 08-Jan-14 A | | |
| P17-2020 | Place Conc @ Core | 0 | 0 | 08-Jan-14 A | | |
| P18-2002 | FRP Columns Below | 5 | 0 | 09-Jan-14 A | 15-Jan-14 A | |
| P18-2000 | Jump/Resteel/Close Core | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P18-2004 | Shore / Form Deck | 3 | 0 | 09-Jan-14 A | 13-Jan-14 A | |
| LL2-2022R | MEP Rough In | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P7-2018 | Remove Reshores | 2 | 0 | 10-Jan-14 A | 13-Jan-14 A | |
| P17-2014 | Stress Tendons | 1 | 0 | 11-Jan-14 A | 11-Jan-14 A | |
| P13–2018 | Remove Reshores | 2 | 0 | 13-Jan-14 A | 14-Jan-14 A | |
| P13A–2018 | Remove Reshores | 2 | 0 | 15-Jan-14 A | 16-Jan-14 A | |
| WEA-2012 | WIND IMPACT | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| P18-2006 | MEP Rough In | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2008 | ReSteel / PT Cables | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2010 | Install Edgeform/Embeds | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2012 | Place / Finish Deck | 0 | 0 | 22-Jan-14 A | | |
| P18-2020 | Place Conc @ Core | 0 | 0 | 22-Jan-14 A | | |
| P19-2002 | FRP Columns Below | 5 | 0 | 23-Jan-14 A | 29-Jan-14 A | |
| P19-2000 | Jump/Resteel/Close Core | 4 | 0 | 23-Jan-14 A | 28-Jan-14 A | |
| P19-2004 | Shore / Form Deck | 3 | 0 | 23-Jan-14 A | 27-Jan-14 A | |
| P18-2014 | Stress Tendons | 1 | 0 | 25-Jan-14 A | 25-Jan-14 A | |
| P14–2018 | Remove Reshores | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2006 | MEP Rough In | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2008 | ReSteel / PT Cables | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2010 | Install Edgeform/Embeds | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2012 | Place / Finish Deck | 0 | 0 | 29-Jan-14 A | | |
| P19-2020 | Place Conc @ Core | 0 | 0 | 29-Jan-14 A | | |
| P20-2002 | FRP Columns Below | 5 | 0 | 30-Jan-14 A | 05-Feb-14 A | |

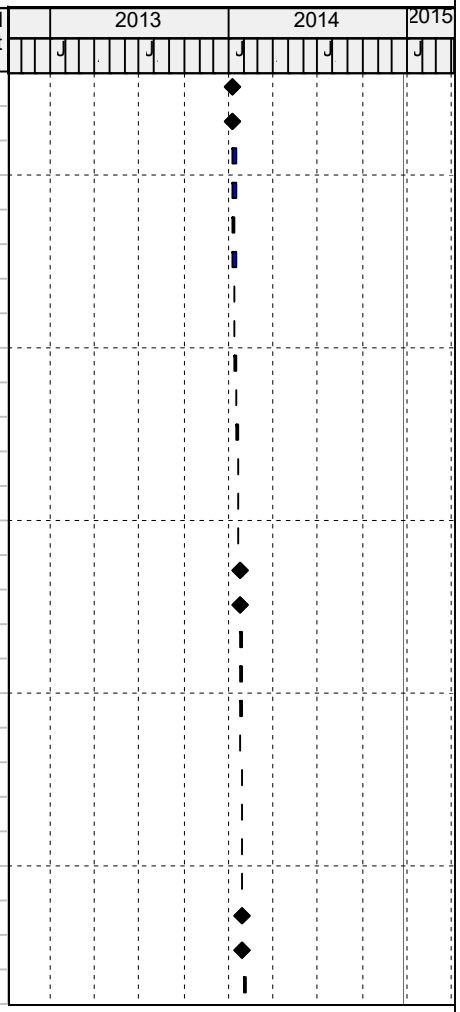



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P20-2000 | Jump/Resteel/Close Core | 9 | 0 | 30-Jan-14 A | 11-Feb-14 A | |
| P20-2004 | Shore / Form Deck | 6 | 0 | 30-Jan-14 A | 10-Feb-14 A | |
| P19-2014 | Stress Tendons | 1 | 0 | 01-Feb-14 A | 01-Feb-14 A | |
| P13A–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P14–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P15–2016 | Strip / ReShore Deck | 3 | 0 | 06-Feb-14 A | 10-Feb-14 A | |
| P20-2006 | MEP Rough In | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2008 | ReSteel / PT Cables | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2010 | Install Edgeform/Embeds | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| L03-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 06-Feb-14 A | 12-Feb-14 A | |
| P16-2016 | Strip / ReShore Deck | 3 | 0 | 10-Feb-14 A | 12-Feb-14 A | |
| L04-2018 | Remove Reshores | 2 | 0 | 10-Feb-14 A | 11-Feb-14 A | |
| L03-2018 | Remove Reshores | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| P17-2016 | Strip / ReShore Deck | 3 | 0 | 12-Feb-14 A | 14-Feb-14 A | |
| P20-2012 | Place / Finish Deck | 0 | 0 | 12-Feb-14 A | | |
| P20-2020 | Place Conc @ Core | 0 | 0 | 12-Feb-14 A | | |
| L04-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-Feb-14 A | 18-Feb-14 A | |
| P12–2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P18-2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P21-2002 | FRP Columns Below | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| P21-2000 | Jump/Resteel/Close Core | 4 | 0 | 13-Feb-14 A | 18-Feb-14 A | |
| P21-2004 | Shore / Form Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P19-2016 | Strip / ReShore Deck | 3 | 0 | 14-Feb-14 A | 18-Feb-14 A | |
| P20-2014 | Stress Tendons | 1 | 0 | 15-Feb-14 A | 15-Feb-14 A | |
| P21-2006 | MEP Rough In | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2008 | ReSteel / PT Cables | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |

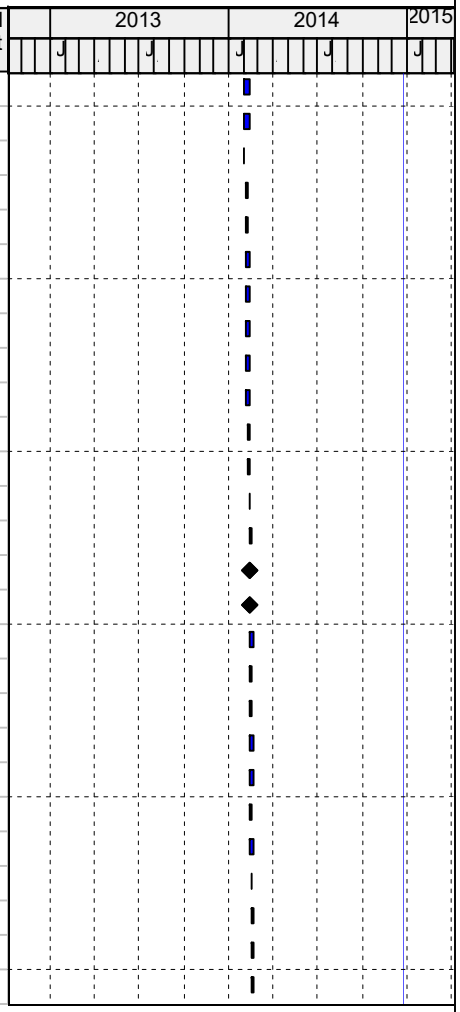



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P20-2016 | Strip / ReShore Deck | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| L05-2018 | Remove Reshores | 2 | 0 | 18-Feb-14 A | 19-Feb-14 A | |
| P21-2012 | Place / Finish Deck | 0 | 0 | 19-Feb-14 A | | |
| P21-2020 | Place Conc @ Core | 0 | 0 | 19-Feb-14 A | | |
| P22-2002 | FRP Columns Below | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P22-2000 | Jump/Resteel/Close Core | 4 | 0 | 20-Feb-14 A | 25-Feb-14 A | |
| P22-2004 | Shore / Form Deck | 3 | 0 | 20-Feb-14 A | 24-Feb-14 A | |
| L05-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P21-2014 | Stress Tendons | 1 | 0 | 22-Feb-14 A | 22-Feb-14 A | |
| P21-2016 | Strip / ReShore Deck | 3 | 0 | 24-Feb-14 A | 26-Feb-14 A | |
| P22-2006 | MEP Rough In | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2008 | ReSteel / PT Cables | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| L06-2018 | Remove Reshores | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| P22-2012 | Place / Finish Deck | 0 | 0 | 26-Feb-14 A | | |
| P22-2020 | Place Conc @ Core | 0 | 0 | 26-Feb-14 A | | |
| P23-2002 | FRP Columns Below | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2000 | Jump/Resteel/Close Core | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2004 | Shore / Form Deck | 3 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2006 | MEP Rough In | 2 | 0 | 01-Mar-14 A | 03-Mar-14 A | |
| P22-2014 | Stress Tendons | 1 | 0 | 01-Mar-14 A | 01-Mar-14 A | |
| P23-2008 | ReSteel / PT Cables | 2 | 0 | 03-Mar-14 A | 04-Mar-14 A | |
| P22-2016 | Strip / ReShore Deck | 3 | 0 | 04-Mar-14 A | 10-Mar-14 A | |
| P23-2010 | Install Edgeform/Embeds | 2 | 0 | 04-Mar-14 A | 04-Mar-14 A | |
| L07-2018 | Remove Reshores | 2 | 0 | 04-Mar-14 A | 05-Mar-14 A | |
| P23-2012 | Place / Finish Deck | 0 | 0 | 05-Mar-14 A | | |
| P23-2020 | Place Conc @ Core | 0 | 0 | 05-Mar-14 A | | |

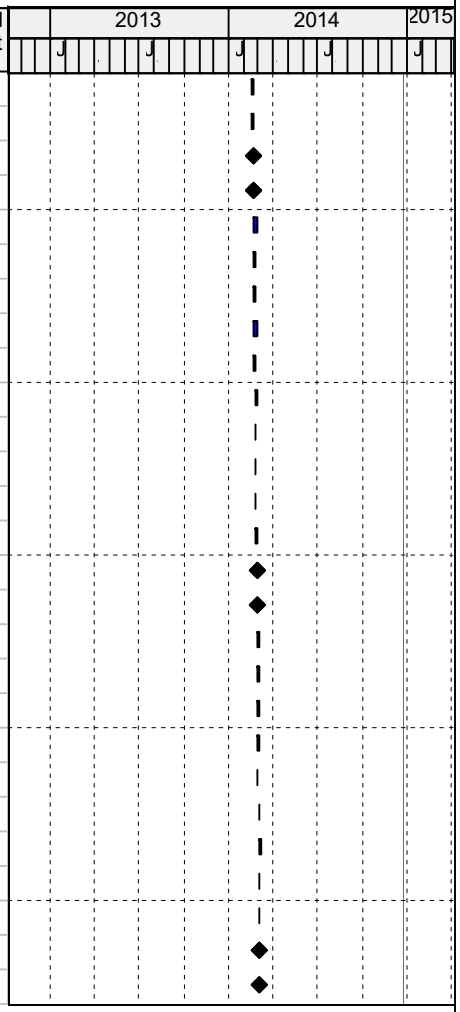


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P24-2002 | FRP Columns Below | 5 | 0 | 05-Mar-14 A | 07-Mar-14 A | |
| P24-2004 | Shore / Form Deck | 3 | 0 | 06-Mar-14 A | 10-Mar-14 A | |
| P24-2000 | Jump/Resteel/Close Core | 4 | 0 | 08-Mar-14 A | 10-Mar-14 A | |
| P23-2014 | Stress Tendons | 1 | 0 | 10-Mar-14 A | 10-Mar-14 A | |
| P24-2008 | ReSteel / PT Cables | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P24-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P23-2016 | Strip / ReShore Deck | 3 | 0 | 11-Mar-14 A | 17-Mar-14 A | |
| P24-2006 | MEP Rough In | 2 | 0 | 11-Mar-14 A | 11-Mar-14 A | |
| P25-2002 | FRP Columns Below | 5 | 0 | 11-Mar-14 A | 13-Mar-14 A | |
| L08-2018 | Remove Reshores | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| P24-2012 | Place / Finish Deck | 0 | 0 | 12-Mar-14 A | | |
| P24-2020 | Place Conc @ Core | 0 | 0 | 12-Mar-14 A | | |
| P25-2004 | Shore / Form Deck | 3 | 0 | 13-Mar-14 A | 17-Mar-14 A | |
| P25-2000 | Jump/Resteel/Close Core | 4 | 0 | 15-Mar-14 A | 17-Mar-14 A | |
| P24-2014 | Stress Tendons | 1 | 0 | 17-Mar-14 A | 17-Mar-14 A | |
| P25-2006 | MEP Rough In | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2008 | ReSteel / PT Cables | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| L06-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 18-Mar-14 A | 20-Mar-14 A | |
| L09-2018 | Remove Reshores | 2 | 0 | 18-Mar-14 A | 19-Mar-14 A | |
| P26-2002 | FRP Columns Below | 5 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| P25-2012 | Place / Finish Deck | 0 | 0 | 19-Mar-14 A | | |
| P25-2020 | Place Conc @ Core | 0 | 0 | 19-Mar-14 A | | |
| P26-2004 | Shore / Form Deck | 3 | 0 | 20-Mar-14 A | 24-Mar-14 A | |
| L07-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 21-Mar-14 A | 25-Mar-14 A | |
| P26-2000 | Jump/Resteel/Close Core | 4 | 0 | 22-Mar-14 A | 24-Mar-14 A | |
| P26-2006 | MEP Rough In | 2 | 0 | 24-Mar-14 A | 24-Mar-14 A | |

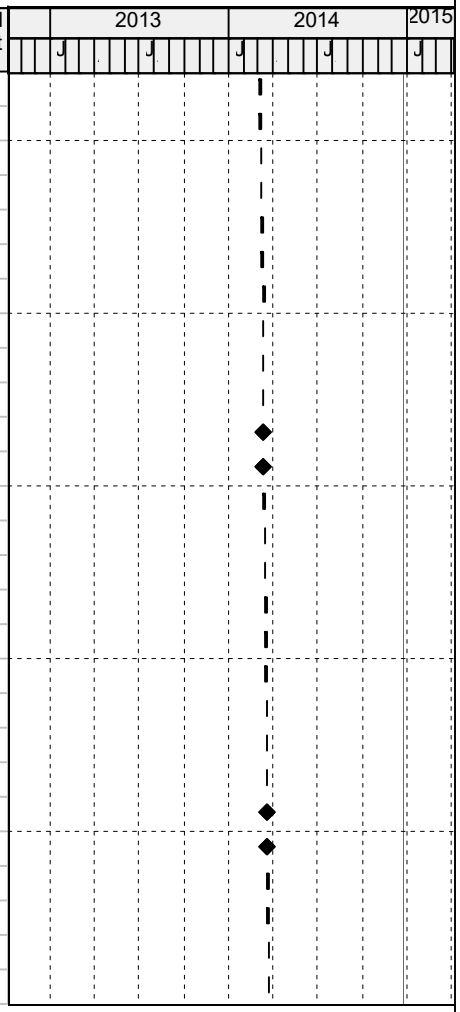


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P26-2008 | ReSteel / PT Cables | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P26-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P25-2014 | Stress Tendons | 1 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P27-2002 | FRP Columns Below | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| P26-2012 | Place / Finish Deck | 0 | 0 | 26-Mar-14 A | | |
| P26-2020 | Place Conc @ Core | 0 | 0 | 26-Mar-14 A | | |
| L08-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 26-Mar-14 A | 28-Mar-14 A | |
| L10-2018 | Remove Reshores | 2 | 0 | 26-Mar-14 A | 27-Mar-14 A | |
| P27-2004 | Shore / Form Deck | 3 | 0 | 27-Mar-14 A | 31-Mar-14 A | |
| P27-2000 | Jump/Resteel/Close Core | 4 | 0 | 29-Mar-14 A | 31-Mar-14 A | |
| P27-2006 | MEP Rough In | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2008 | ReSteel / PT Cables | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2010 | Install Edgeform/Embeds | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P26-2014 | Stress Tendons | 1 | 0 | 31-Mar-14 A | 31-Mar-14 A | |
| L09-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 31-Mar-14 A | 02-Apr-14 A | |
| P24-2016 | Strip / ReShore Deck | 3 | 0 | 01-Apr-14 A | 07-Apr-14 A | |
| L11-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 02-Apr-14 A | |
| L12-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 03-Apr-14 A | |
| P27-2012 | Place / Finish Deck | 0 | 0 | 02-Apr-14 A | | |
| P27-2020 | Place Conc @ Core | 0 | 0 | 02-Apr-14 A | | |
| P28-2002 | FRP Columns Below | 5 | 0 | 02-Apr-14 A | 04-Apr-14 A | |
| P28-2004 | Shore / Form Deck | 4 | 0 | 03-Apr-14 A | 08-Apr-14 A | |
| L10-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| P27-2014 | Stress Tendons | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| P25-2016 | Strip / ReShore Deck | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L14-2018 | Remove Reshores | 2 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| P28-2000 | Jump/Resteel/Close Core | 7 | 0 | 08-Apr-14 A | 11-Apr-14 A | |

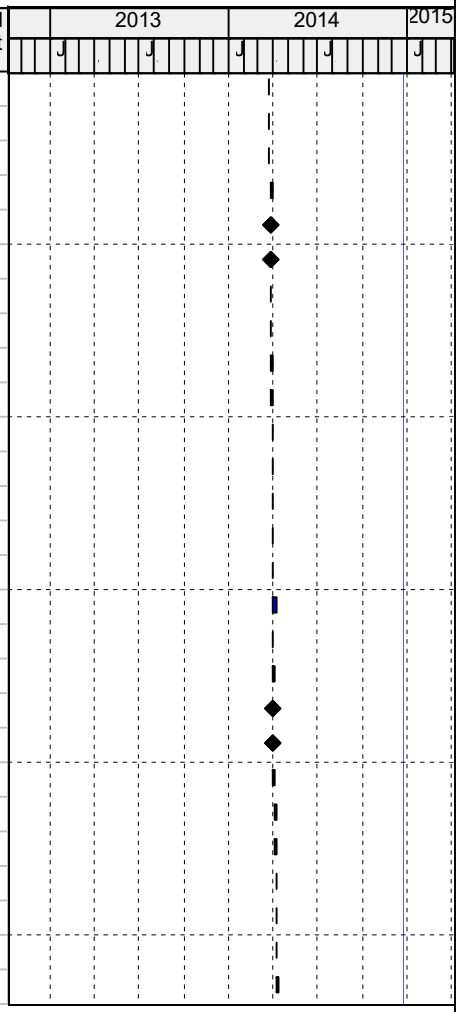



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P28-2006 | MEP Rough In | 4 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2008 | ReSteel / PT Cables | 4 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Apr-14 A | 11-Apr-14 A | |
| L12-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| P28-2012 | Place / Finish Deck | 0 | 0 | 14-Apr-14 A | | |
| P28-2020 | Place Conc @ Core | 0 | 0 | 14-Apr-14 A | | |
| P29-2002 | FRP Columns Above Roof Deck | 3 | 0 | 14-Apr-14 A | 18-Apr-14 A | |
| P26-2016 | Strip / ReShore Deck | 3 | 0 | 14-Apr-14 A | 17-Apr-14 A | |
| L14-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-Apr-14 A | 18-Apr-14 A | |
| P28-2014 | Stress Tendons | 1 | 0 | 17-Apr-14 A | 17-Apr-14 A | |
| P29-2000 | Strip Core | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| P27-2016 | Strip / ReShore Deck | 3 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L15-2018 | Remove Reshores | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| P28-2016 | Strip / ReShore Deck | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L15-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L16-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-May-14 A | 19-May-14 A | |
| L16-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2019 | Grind Ceiling for Skim Coat | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| **Ballroom Catwalk & Roof** | | | | | | |
| PC-2100 | Erect Structural Steel @ Porte Cochere | 3 | 0 | 30-Jan-14 A | 03-Feb-14 A | |
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 7 | 0 | 07-Feb-14 A | 17-Feb-14 A | |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| PC-2102 | Metal Decking @ Porte Cochere/ Roof | 2 | 0 | 17-Apr-14 A | 18-Apr-14 A | |
| BR-2112 | BR - Fireproofing @ Structural Steel | 2 | 0 | 27-May-14 A | 30-May-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |

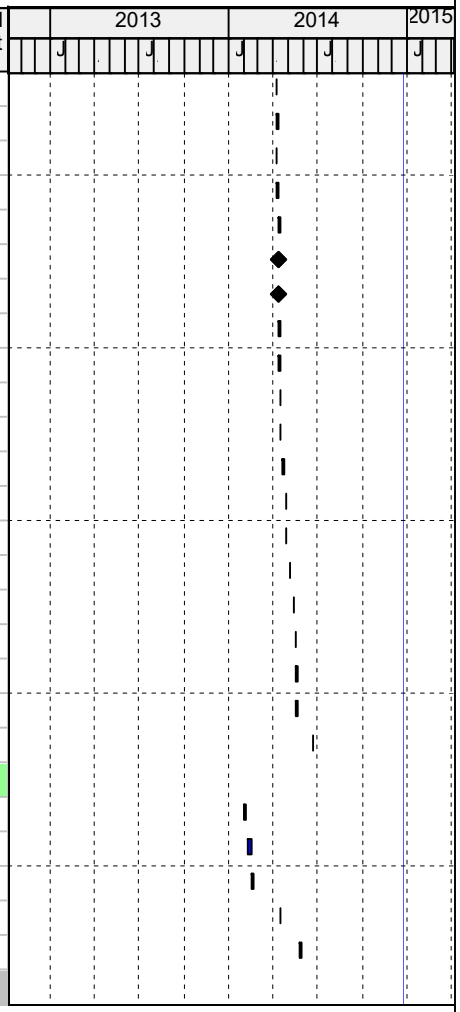


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Mech Penthouse** | | | | | | |
| PH-8706 | Set Mech Equipment @ Tower Roof | 3 | 0 | 22-May-14 A | 28-May-14 A | |
| PH-8708 | Set Equipment @ Penthouse | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| PH-8700 | PH - Structural Steel and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| **Vertical Circulation** | | | | | | |
| **Stairs** | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 25-Nov-13 A | 26-Nov-13 A | |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 27-Nov-13 A | 03-Dec-13 A | |
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 04-Dec-13 A | 05-Dec-13 A | |
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 06-Dec-13 A | 09-Dec-13 A | |
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 2 | 0 | 03-Feb-14 A | 04-Feb-14 A | |
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 2 | 0 | 06-Feb-14 A | 07-Feb-14 A | |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 2 | 0 | 07-Feb-14 A | 07-Feb-14 A | |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 2 | 0 | 07-Feb-14 A | 10-Feb-14 A | |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 2 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 2 | 0 | 06-Mar-14 A | 07-Mar-14 A | |
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 2 | 0 | 07-Mar-14 A | 10-Mar-14 A | |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 2 | 0 | 13-Mar-14 A | 14-Mar-14 A | |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 2 | 0 | 08-Apr-14 A | 21-Apr-14 A | |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 2 | 0 | 27-May-14 A | 28-May-14 A | |

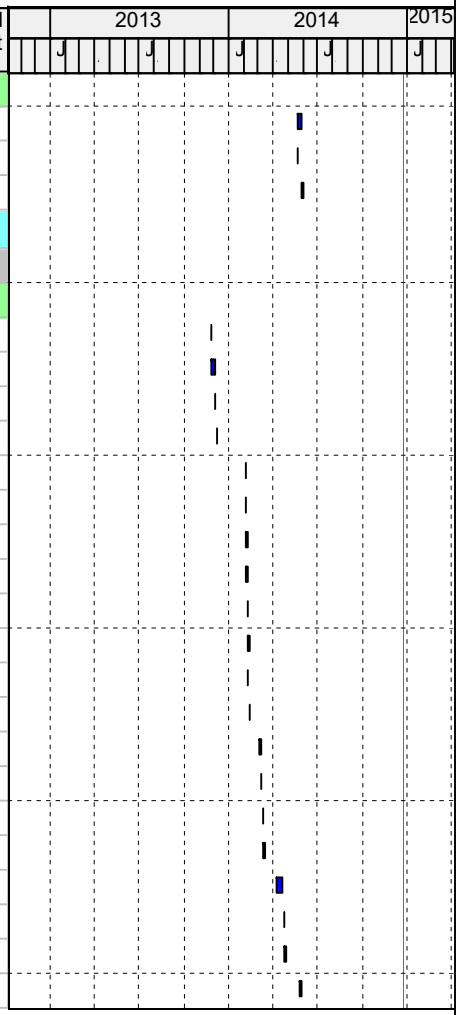



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S1-4040 | Stair 1 - Set Mtl Stairs / Railings L18 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 10-Dec-13 A | 11-Dec-13 A | |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 12-Dec-13 A | 13-Dec-13 A | |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 16-Dec-13 A | 17-Dec-13 A | |
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 18-Dec-13 A | 19-Dec-13 A | |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 2 | 0 | 12-Feb-14 A | 13-Feb-14 A | |
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 2 | 0 | 13-Feb-14 A | 13-Feb-14 A | |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 2 | 0 | 13-Feb-14 A | 14-Feb-14 A | |
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 2 | 0 | 19-Feb-14 A | 20-Feb-14 A | |
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 2 | 0 | 21-Feb-14 A | 24-Feb-14 A | |
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 2 | 0 | 19-Mar-14 A | 20-Mar-14 A | |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 2 | 0 | 21-Mar-14 A | 22-Mar-14 A | |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 2 | 0 | 14-May-14 A | 15-May-14 A | |
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 2 | 0 | 16-May-14 A | 19-May-14 A | |
| S2-4038 | Stair 2 - Set Mtl Stairs / Railings L17 | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - Set Metal Stairs / Railings LL2 | 6 | 0 | 05-Mar-14 A | 20-Mar-14 A | |
| S3-4002 | Stair 3 - Set Metal Stairs / Railings LL1 | 6 | 0 | 17-Mar-14 A | 21-Mar-14 A | |
| S3-4004 | Stair 3 - Permanent Railings / Final Finishes | 4 | 4 | 02-Feb-15 | 05-Feb-15 | 28 |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |

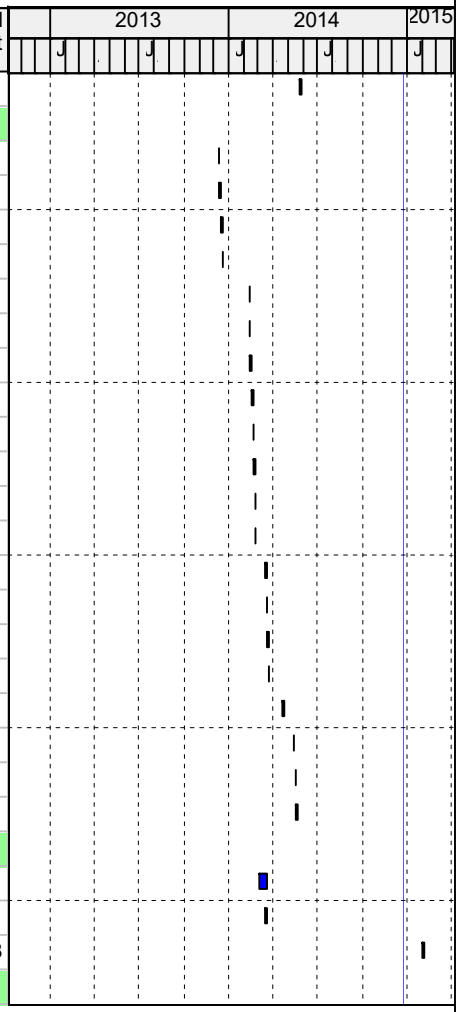



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S4-4000 | Stair 4 - Set Metal Stairs / Railings LL2 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4002 | Stair 4 - Set Metal Stairs / Railings LL1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4004 | Stair 4 -Set Metal Stairs / Railings L1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4006 | Stair 4 - Permanent Railings / Final Finishes | 4 | 4 | 26-Jan-15 | 29-Jan-15 | 31 |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |
| S6-4000 | Stair 6 - Set Metal Stairs / Railings | 5 | 0 | 25-Jun-14 A | 01-Jul-14 A | |
| S6-4002 | Stair 6 - Permanent Railings / Final Finishes | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 35 |
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes | 5 | 5 | 16-Feb-15 | 20-Feb-15 | 17 |
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a -Set Metal Stairs / Railings L1 | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| S4a-4002 | Stair 4a - Permanent Railings / Final Finishes | 2 | 2 | 30-Jan-15 | 02-Feb-15 | 31 |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 07-Jun-13 A | | |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 0 | 17-Jun-13 A | 21-Jun-13 A | |
| EL-1004 | Elev - Submittal Approval | 21 | 0 | 21-Jun-13 A | 01-Jan-14 A | |
| EL-1006 | Elev - Release to Manufacturing | 14 | 0 | 02-Jan-14 A | 15-Jan-14 A | |
| EL-1008 | Elev - Fabrication (Engineered Geared) | 95 | 0 | 16-Jan-14 A | 14-Jun-14 A | |
| EL-1010 | Elev - Machines delivered | 1 | 0 | 12-May-14 A | 12-May-14 A | |
| EL-1011 | Elev - Elevator Machines Flown & Set At Top Of Hoist | 5 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5016 | Elev 5 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-1216 | Elev 1&2 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-3416 | Elev 3&4 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |

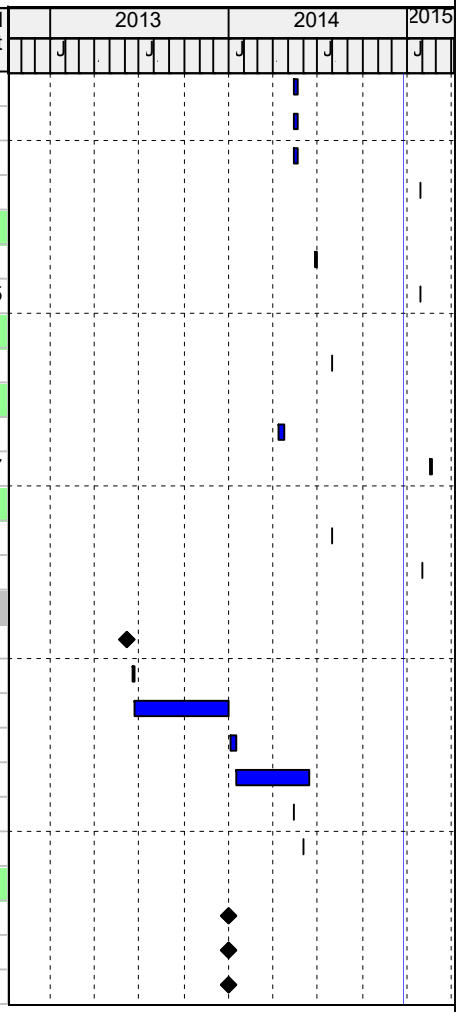


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-1202 | Elev 1&2 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-3402 | Elev 3&4 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-5018 | Elev 5 - Set Hoistway Machines | 3 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| EL-1218 | Elev 1&2 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-3418 | Elev 3&4 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-1200 | Elev 1&2 - Hoistway Clear & Ready (GC) | 0 | 0 | 20-Jun-14 A | | |
| EL-1204 | Elev 1&2 - Install Rails & Brackets | 17 | 0 | 23-Jun-14 A | 15-Jul-14 A | |
| EL-3400 | Elev 3&4 - Hoistway Clear & Ready (GC) | 0 | 0 | 23-Jun-14 A | | |
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 24-Jun-14 A | | |
| EL-1206 | Elev 1&2 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Jul-14 A | |
| EL-1207 | Elev 1&2 - Install Pit Equipment/Car Sling/CWT Fram | 3 | 0 | 15-Jul-14 A | 01-Aug-14 A | |
| EL-1208 | Elev 1&2 - Install MHoist & Cable | 5 | 0 | 16-Jul-14 A | 24-Jul-14 A | |
| EL-3407 | Elev 3&4 - Install Pit Equipment/Car Sling/CWT Fram | 5 | 0 | 16-Jul-14 A | 06-Aug-14 A | |
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 21-Jul-14 A | | |
| EL-5004 | Elev 5 - Install Rails & Brackets | 13 | 0 | 21-Jul-14 A | 11-Aug-14 A | |
| EL-3404 | Elev 3&4 - Install Rails & Brackets | 18 | 0 | 23-Jul-14 A | 04-Aug-14 A | |
| EL-3406 | Elev 3&4 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 28-Jul-14 A | |
| EL-3408 | Elev 3&4 - Install Hoist & Cable | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| EL-5007 | Elev 5 - Install Pit Equipment/Car Sling/CWT Frame/V | 5 | 0 | 12-Aug-14 A | 15-Aug-14 A | |
| EL-1210 | Elev 1&2 - Install Entrances/Doors/Fixtures/Fascia | 19 | 0 | 14-Aug-14 A | 22-Sep-14 A | |
| EL-3410 | Elev 3&4 - Install Entrances/Doors/Fixtures/Fascia | 30 | 0 | 14-Aug-14 A | 02-Oct-14 A | |
| EL-5006 | Elev 5 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Aug-14 A | |
| EL-5008 | Elev 5 - Install MHoist & Cable | 4 | 0 | 18-Aug-14 A | 20-Aug-14 A | |
| EL-5010 | Elev 5 - Install Entrances/Doors/Fixtures/Fascia | 21 | 0 | 21-Aug-14 A | 26-Sep-14 A | |
| EL-1212 | Elev 1&2 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 22-Sep-14 A | 13-Oct-14 A | |
| EL-5012 | Elev 5 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 26-Sep-14 A | 16-Oct-14 A | |

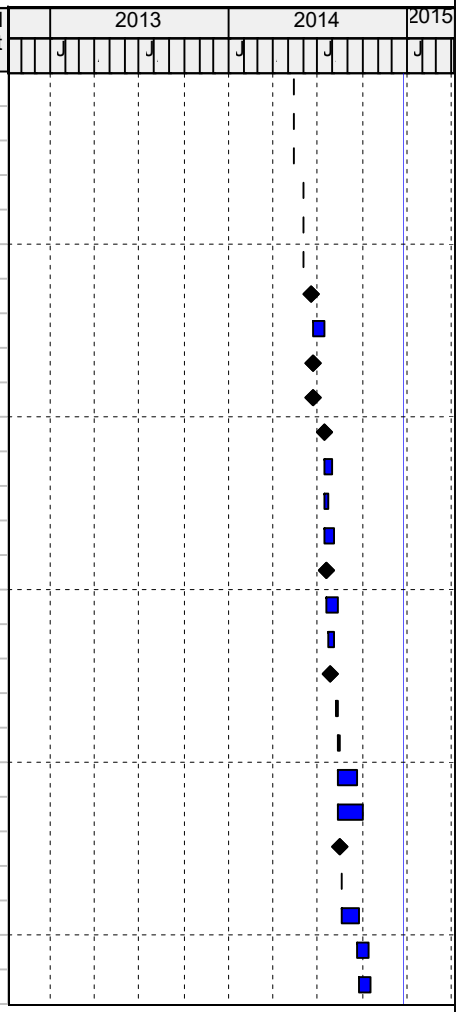


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-3412 | Elev 3&4 - Install Hoistway Equipment/Pipe & Wire | 23 | 0 | 03-Oct-14 A | 03-Nov-14 A | |
| EL-1214 | Elev 1&2 - Install Cab/Wiring/Door Operator(s) | 11 | 0 | 14-Oct-14 A | 28-Oct-14 A | |
| EL-5014 | Elev 5 - Install Cab/Wiring/Door Operator(s) | 7 | 0 | 17-Oct-14 A | 27-Oct-14 A | |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 1 | 0 | 24-Oct-14 A | 24-Oct-14 A | |
| EL-6016 | Elev 6 - Hoistway Walls Complete (GC) | 0 | 0 | | 24-Oct-14 A | |
| EL-6004 | Elev 6 - Install Cylinders/Rails & Brackets | 4 | 0 | 27-Oct-14 A | 30-Oct-14 A | |
| EL-5022 | Elev 5 - Adjust | 5 | 0 | 28-Oct-14 A | 03-Nov-14 A | |
| EL-1222 | Elev 1&2 - Adjust | 5 | 0 | 29-Oct-14 A | 04-Nov-14 A | |
| EL-6006 | Elev 6 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 30-Oct-14 A | |
| EL-6007 | Elev 6 - Install Pit Equipment/Car Sling | 2 | 0 | 31-Oct-14 A | 03-Nov-14 A | |
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| EL-3414 | Elev 3&4 - Install Cab/Wiring/Door Operator(s) | 10 | 0 | 04-Nov-14 A | 17-Nov-14 A | |
| EL-6018 | Elev 6 - Install Machine Room Equipment | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| EL-1224 | Elev 1&2 - Clean / Paint / Punchlist | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| EL-5026 | Elev 5 - Inspections | 7 | 0 | 13-Nov-14 A | 14-Nov-14 A | |
| EL-3422 | Elev 3&4 - Adjust | 8 | 0 | 18-Nov-14 A | 20-Nov-14 A | |
| EL-6012 | Elev 6 - Install hoistway rails & divider beams | 2 | 0 | 20-Nov-14 A | 21-Nov-14 A | |
| EL-6010 | Elev 6 - Install elevator fronts/rears | 9 | 4 | 09-Dec-14 A | 29-Dec-14 | 33 |
| EL-6014 | Elev 6 - Cab build-out | 5 | 1 | 15-Dec-14 A | 22-Dec-14 | 32 |
| EL-3424 | Elev 3&4 - Walsh/TKE pre-inspection | 6 | 6 | 22-Dec-14 | 31-Dec-14 | 41 |
| EL-1226 | Elev 1&2 - CoB/L&I Inspections | 5 | 5 | 02-Jan-15* | 08-Jan-15 | 41 |
| EL-3426 | Elev 3&4 - CoB/L&I Inspections | 5 | 5 | 02-Jan-15 | 08-Jan-15 | 41 |
| EL-6022 | Elev 6 - Final cleaning at EMR | 4 | 4 | 08-Jan-15 | 13-Jan-15 | 32 |
| EL-6024 | Elev 6 - Walsh/TKE pre-inspection | 2 | 2 | 14-Jan-15 | 15-Jan-15 | 32 |
| EL-6026 | Elev 6 - CoB/L&I Inspections | 1 | 1 | 16-Jan-15 | 16-Jan-15 | 32 |
| **Exterior Shell** | | | | | | |
| Elevations | | | | | | |

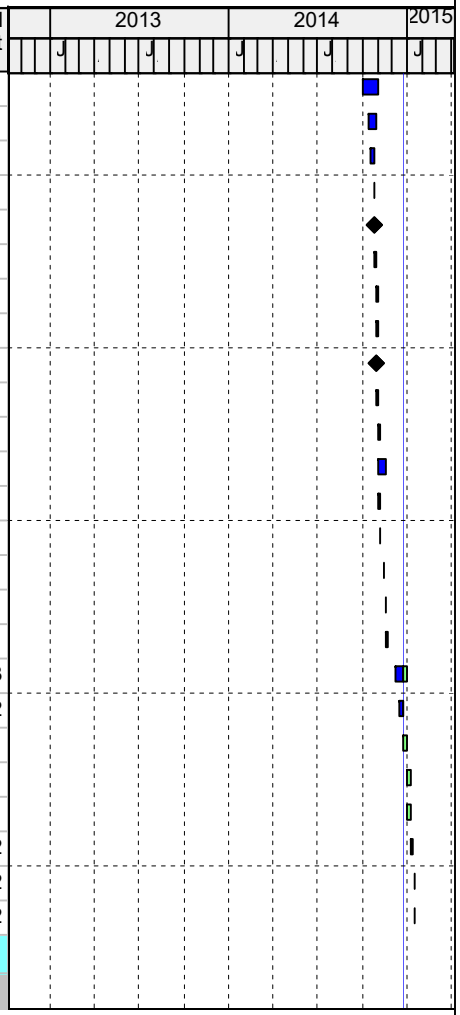



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2** | | | | | | |
| L3D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Feb-14 A | 12-Feb-14 A | |
| L3-5308 | L3- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 17-Feb-14 A | 21-Feb-14 A | |
| L4D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Feb-14 A | 19-Feb-14 A | |
| L4-5308 | L4- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Feb-14 A | 28-Feb-14 A | |
| L5D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Feb-14 A | 26-Feb-14 A | |
| L5-5308 | L5- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 03-Mar-14 A | 07-Mar-14 A | |
| L6D5308 | Deliver/Stock Wall Panels | 1 | 0 | 05-Mar-14 A | 05-Mar-14 A | |
| L6-5308 | L6- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L7-5308 | L7- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L7D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Mar-14 A | 12-Mar-14 A | |
| L8D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Mar-14 A | 19-Mar-14 A | |
| L8-5308 | L8- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Mar-14 A | 28-Mar-14 A | |
| L9D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L9-5308 | L9- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 31-Mar-14 A | 07-Apr-14 A | |
| 10D5308 | Deliver/Stock Wall Panels | 1 | 0 | 02-Apr-14 A | 02-Apr-14 A | |
| L10-5308 | L10- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 07-Apr-14 A | 11-Apr-14 A | |
| 11D5308 | Deliver/Stock Wall Panels | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L11-5308 | L11- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 11-Apr-14 A | 18-Apr-14 A | |
| 12D5308 | Deliver/Stock Wall Panels | 1 | 0 | 16-Apr-14 A | 16-Apr-14 A | |
| L12-5308 | L12- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Apr-14 A | 25-Apr-14 A | |
| 14D5308 | Deliver/Stock Wall Panels | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L14-5308 | L14 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Apr-14 A | 01-May-14 A | |
| 15D5308 | Deliver/Stock Wall Panels | 1 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L15-5308 | L15 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| 16D5308 | Deliver/Stock Wall Panels | 1 | 0 | 07-May-14 A | 07-May-14 A | |

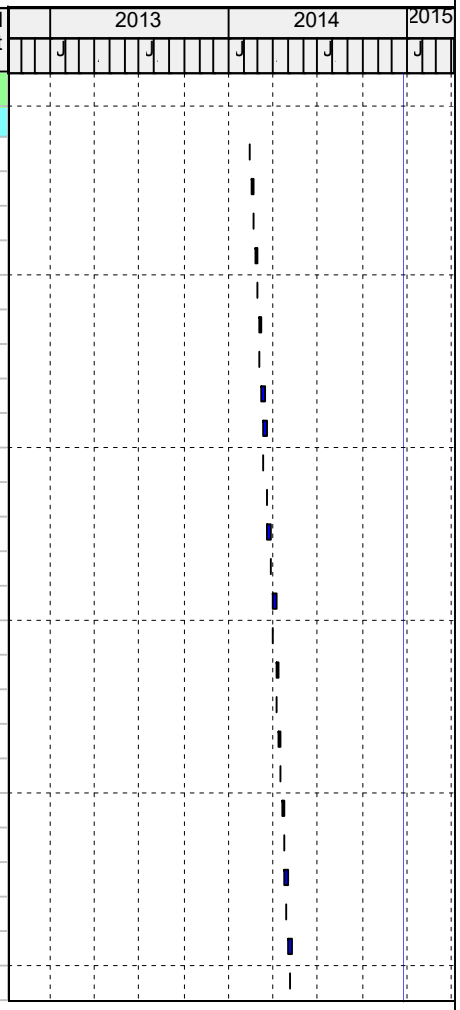


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-5308 | L16- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| 17D5308 | Deliver/Stock Wall Panels | 1 | 0 | 14-May-14 A | 14-May-14 A | |
| L17-5308 | L17 - Support Frame/Sheathing for Metal Wall Panel | 5 | 0 | 20-May-14 A | 11-Jun-14 A | |
| LL2-5308 | LL2 Thru L4 - Support Frame/Sheathing for Metal Wa | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL1-5308 | LL1 - Support Frame/Sheathing for Metal Wall Panel | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| L1-5308 | L1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| **Level 1** | | | | | | |
| L3-5102 | L3- Storefront Frames | 7 | 0 | 18-Aug-14 A | 29-Sep-14 A | |
| L1-5102 | L1 - Storefront Frames (excl. Main Entry Facade) | 8 | 0 | 02-Sep-14 A | 11-Sep-14 A | |
| L1-5104 | L1 - Storefront Glazing (excl. Main Entry Facade) | 4 | 0 | 19-Sep-14 A | 24-Sep-14 A | |
| EP-5110 | L1 - Revolving Doors | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L3-5104 | L3 - Storefront Glazing | 3 | 0 | 30-Sep-14 A | 03-Oct-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Levels 3-4** | | | | | | |
| L3-5130 | L3 - Install Punch Windows | 5 | 0 | 24-Feb-14 A | 10-Mar-14 A | |
| L4-5130 | L4 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 12-Mar-14 A | |
| L5-5130 | L5 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L6-5130 | L6- Install Punch Windows | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L7-5130 | L7 - Install Punch Windows | 5 | 0 | 18-Mar-14 A | 21-Mar-14 A | |
| L8-5130 | L8 - Install Punch Windows | 5 | 0 | 24-Mar-14 A | 28-Mar-14 A | |
| L9-5130 | L9 - Install Punch Windows | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L10-5130 | L10 - Install Punch Windows | 5 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-5130 | L11 - Install Punch Windows | 5 | 0 | 14-Apr-14 A | 21-Apr-14 A | |
| L12-5130 | L12 - Install Punch Windows | 5 | 0 | 22-Apr-14 A | 25-Apr-14 A | |
| L14-5130 | L14 - Install Punch Windows | 5 | 0 | 28-Apr-14 A | 05-May-14 A | |
| L15-5130 | L15 - Install Punch Windows | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| L16-5130 | L16 - Install Punch Windows | 5 | 0 | 12-May-14 A | 20-May-14 A | |

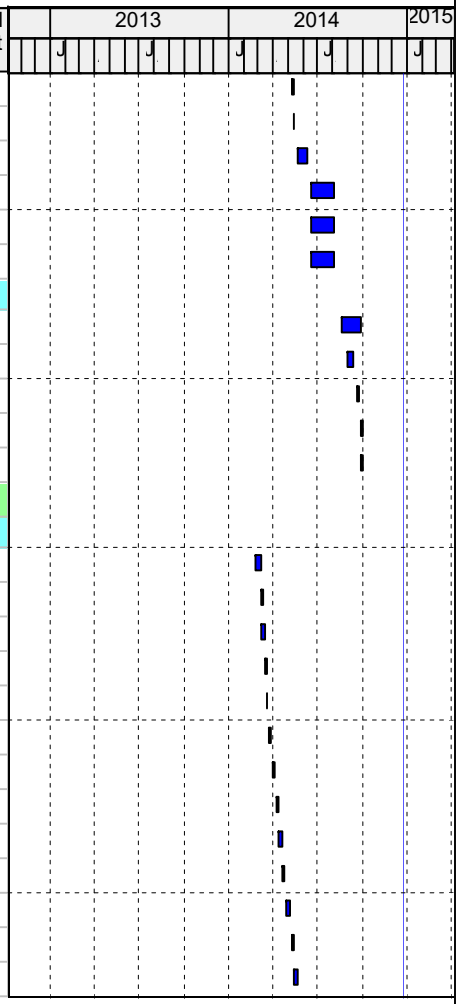



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-5130 | L17 - Install Punch Windows | 5 | 0 | 27-May-14 A | 16-Jun-14 A | |
| Roofs | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| RF-4026 | L1 - City Park - Protection Board | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| **Pool Membrane - (elev 18')** | | | | | | |
| RF-4034 | Pool - Install plumbing | 3 | 0 | 20-Oct-14 A | 22-Oct-14 A | |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |
| RF-4010 | AR - Set Mechanical Equipment | 5 | 0 | 10-Jun-14 A | 12-Jun-14 A | |
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 10 | 0 | 04-Aug-14 A | 27-Aug-14 A | |
| RF-4012 | L2.5 Horseshoe - Install corrugated metal panels | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 8 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |
| PC-4008 | RF - Entry / Porte Cochere Roofing System | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | RF - Upper Ballroom Roofing System | 3 | 0 | 28-Jul-14 A | 31-Jul-14 A | |
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 4 | 0 | 31-Jul-14 A | 04-Aug-14 A | |
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |
| RF-4018 | TR - Terrace Roof - Green Roofing System | 5 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| RF-4020 | TR - Terrace Roof - Install sheet metal capping[DELE | 1 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4022 | TR - Terrace Roof - Install deocrative metal railing | 3 | 3 | 17-Feb-15 | 19-Feb-15 | 20 |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Perimeter Framing / Sul | 10 | 0 | 02-Jun-14 A | 08-Jul-14 A | |
| RF-4002 | Tower Roof - Roofing System | 10 | 0 | 20-Aug-14 A | 17-Sep-14 A | |

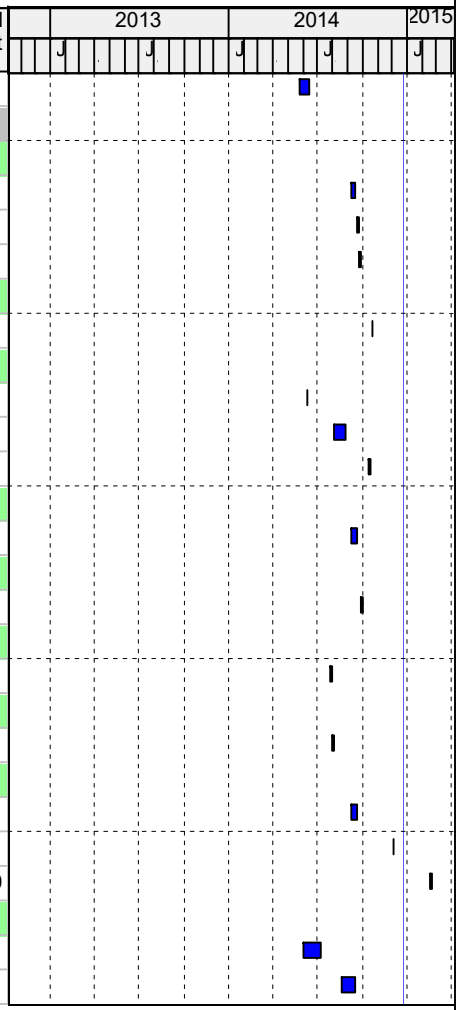



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **PH - Roof - (elev 173')** | | | | | | |
| RF-4030 | PH - Roofing System | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| RF-4032 | PH - Coping / Flashing [DELETED] | 3 | 0 | 01-Sep-14 A | 01-Sep-14 A | |
| **Rough-In's** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6002 | LL4 - Layout | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| LL4-6008 | LL4 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL4-6012 | LL4 - Fire Sprinkler Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6014 | LL4 - Plumbing Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6018 | LL4 - HVAC Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6004 | LL4 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL4-6016 | LL4 - Electrical Rl | 10 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties Rl | 8 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6010 | LL4 - Elevator pits | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| LL4-6020 | LL4 - H Mtl Frames | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL4-6024 | LL4 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6002 | LL3 - Layout | 1 | 0 | 19-Nov-13 A | 19-Nov-13 A | |
| LL3-6008 | LL3 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL3-6012 | LL3 - Fire Sprinkler Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6014 | LL3 - Plumbing Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6018 | LL3 - HVAC Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6004 | LL3 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL3-6020 | LL3 - H Mtl Frames | 3 | 0 | 08-May-14 A | 09-May-14 A | |
| LL3-6010 | LL3 - F/P Curbs | 5 | 0 | 19-May-14 A | 19-May-14 A | |

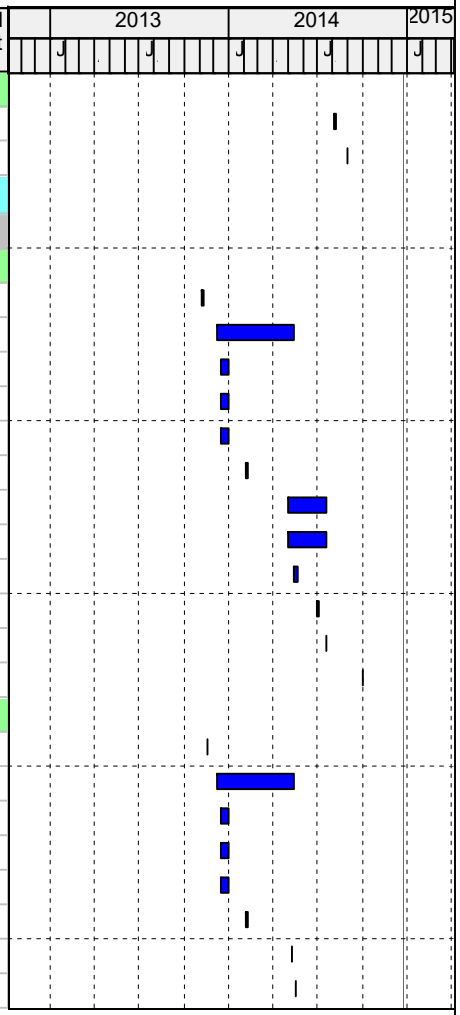



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-6016 | LL3 - Electrical RI | 2 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties RI | 8 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL3-6024 | LL3 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6002 | LL2 - Layout | 1 | 0 | 14-Jan-14 A | 14-Jan-14 A | |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| LL2-6012 | LL2 - Fire Sprinkler RI | 10 | 0 | 21-Jan-14 A | 03-Feb-14 A | |
| LL2-6014 | LL2 - Plumbing RI | 10 | 0 | 21-Jan-14 A | 14-Feb-14 A | |
| LL2E-6016 | LL2 - Electrical RI | 8 | 0 | 03-Feb-14 A | 17-Mar-14 A | |
| LL2-6016 | LL2 - Electrical RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2-6018 | LL2 - HVAC RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2–6004 | LL2 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL2E-6004 | LL2 - CMU Walls | 10 | 0 | 04-Mar-14 A | 09-May-14 A | |
| LL2E-6012 | LL2 - Fire Sprinkler RI | 8 | 0 | 21-Mar-14 A | 01-Apr-14 A | |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 24-Apr-14 A | |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 3 | 0 | 23-Apr-14 A | 21-Jul-14 A | |
| LL2E-6020 | LL2 - H Mtl Frames | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| LL2-6020 | LL2 - H Mtl Frames | 3 | 0 | 12-May-14 A | 13-May-14 A | |
| LL2E-6008 | LL2 - Int Wall Framing | 5 | 0 | 13-May-14 A | 22-Jun-14 A | |
| LL2E-6014 | LL2 - Plumbing RI | 8 | 0 | 13-May-14 A | 30-May-14 A | |
| LL2E-6018 | LL2 - HVAC RI | 8 | 0 | 13-May-14 A | 04-Aug-14 A | |
| LL2E-6022 | LL2 - Fire Alarm / Elec Specialties RI (East of 10) | 8 | 0 | 13-May-14 A | 22-Sep-14 A | |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties RI (West of 10) | 8 | 0 | 19-May-14 A | 22-Sep-14 A | |
| LL2-6015 | LL2 - Main Elect Room Set Equip / RI - Power to Ma | 15 | 0 | 30-Jun-14 A | 26-Sep-14 A | |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 0 | 16-Jul-14 A | 21-Jul-14 A | |
| LL2-6024 | LL2 - Inspections | 2 | 0 | 15-Sep-14 A | 03-Oct-14 A | |

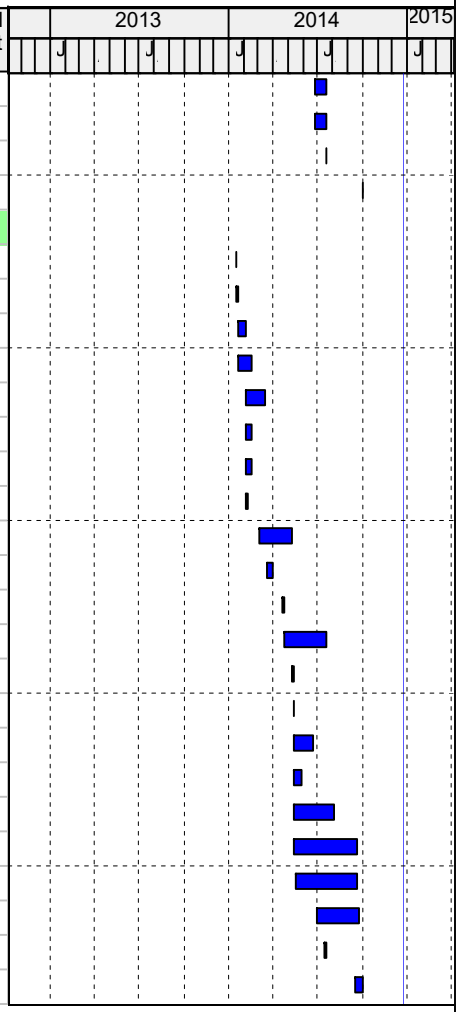



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-6010 | LL2 - F/P Curbs @ Parking | 4 | 4 | 22-Dec-14 | 29-Dec-14 | 44 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6002 | Layout | 3 | 0 | 03-Jan-14 A | 08-Jan-14 A | |
| LL1-6008 | Int Wall Framing & Inspection | 6 | 0 | 08-Jan-14 A | 21-Jul-14 A | |
| LL1-Z2-6002 | Layout | 3 | 0 | 08-Jan-14 A | 14-Jan-14 A | |
| LL1-Z3-6002 | Layout | 3 | 0 | 14-Jan-14 A | 17-Jan-14 A | |
| LL1-Z2-6008 | Int Wall Framing & Inspection | 6 | 0 | 17-Jan-14 A | 01-Aug-14 A | |
| LL1-Z3-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-Jan-14 A | 04-Aug-14 A | |
| LL1-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 09-May-14 A | |
| LL1-Z2-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 28-Apr-14 A | |
| LL1-Z3-6004 | CMU Walls (At All Areas North of Q-Line) | 3 | 0 | 03-Feb-14 A | 13-May-14 A | |
| LL1C-6012 | Complete Fire Sprinkler RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6016 | Complete Electrical RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 10 | 0 | 17-Feb-14 A | 16-Sep-14 A | |
| LL1C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 30-Apr-14 A | |
| LL1-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-Z2-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z2-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z3-6012 | Fire Sprinkler RI (At All Areas North of Q-Line) | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |

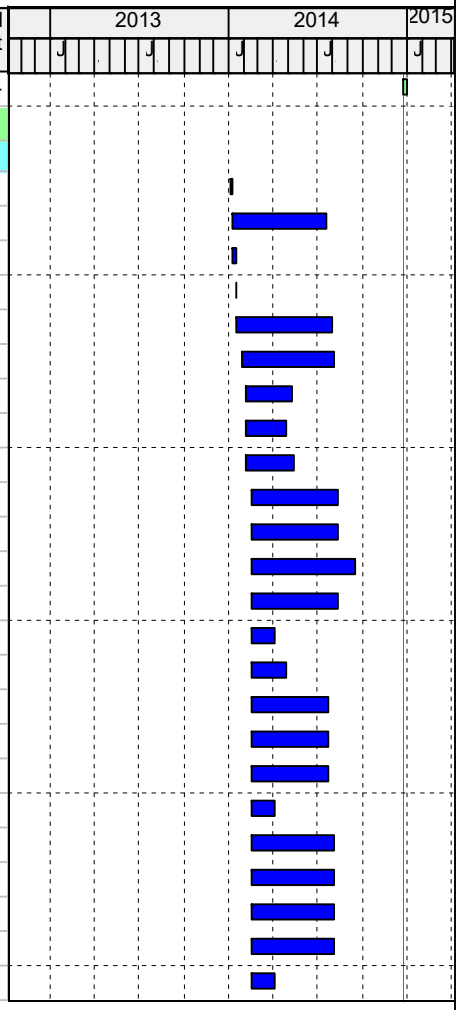



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 11-Sep-14 A | |
| LL1-Z3-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z2C-6012 | Complete Fire Sprinkler RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6014 | Complete Plumbing RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6016 | Complete Electrical RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 15 | 0 | 24-Feb-14 A | 15-Sep-14 A | |
| LL1-Z2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2-6020 | Hollow Metal Door Frames | 5 | 0 | 17-Mar-14 A | 04-Apr-14 A | |
| LL1-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| LL1-Z3-6020 | Hollow Metal Door Frames (At All Areas North of Q-Lir | 1 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| L1B-6004 | CMU Walls [including East Service Corridor] | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L1L-6002 | Layout [including back of house] | 3 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 29-Apr-14 A | |
| L1B-6008 | Int Wall Framing & Inspection | 6 | 0 | 21-Apr-14 A | 08-Aug-14 A | |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 5 | 0 | 25-Apr-14 A | 21-Jul-14 A | |
| LL1C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L1K-6004 | CMU Walls [including public restroom] | 3 | 0 | 05-May-14 A | 08-May-14 A | |
| L1K-6002 | Layout [including public restroom] | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| L1K-6008 | Int Wall Framing & Inspection | 4 | 0 | 09-May-14 A | 22-Aug-14 A | |
| L1B-6002 | Layout [including East Service Corridor] | 3 | 0 | 14-May-14 A | 27-May-14 A | |
| L1L-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-May-14 A | 06-Oct-14 A | |
| L1L-6004 | CMU Walls [including back of house] | 3 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L1K-6012 | Fire Sprinkler RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6014 | Plumbing RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6016 | Electrical RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |

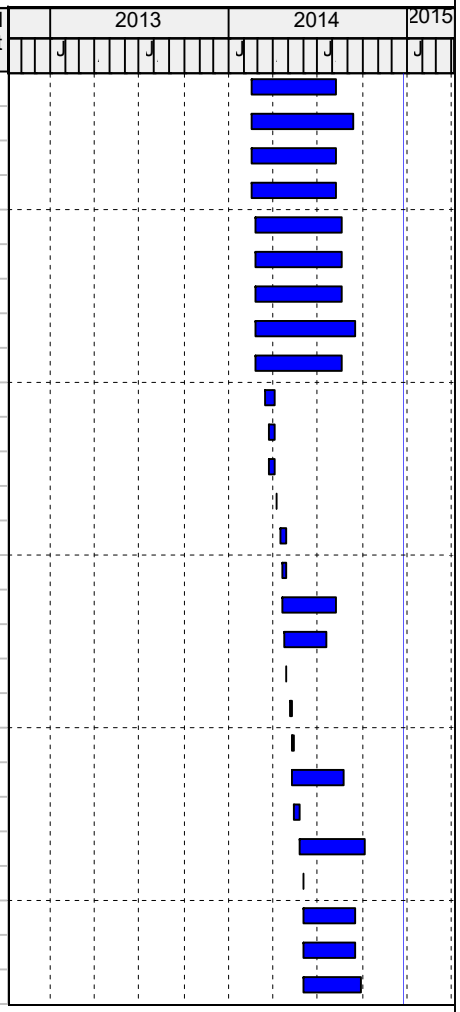


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-6018 | HVAC RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1B-6014 | Plumbing RI [including East Service Corridor] | 10 | 0 | 16-Jun-14 A | 24-Jun-14 A | |
| L1B-6018 | HVAC RI | 10 | 0 | 20-Jun-14 A | 15-Aug-14 A | |
| L1B-6012 | Fire Sprinkler RI | 10 | 0 | 21-Jun-14 A | 15-Aug-14 A | |
| L1L-6018 | HVAC RI | 5 | 0 | 23-Jun-14 A | 13-Oct-14 A | |
| L1L-6014 | Plumbing RI | 5 | 0 | 24-Jun-14 A | 28-Oct-14 A | |
| L1L-6010 | CMU Seismic Clips [including back of house] [DELET | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1L-6012 | Fire Sprinkler RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |
| L1L-6016 | Electrical RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |
| L1L-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 27-Jun-14 A | 13-Oct-14 A | |
| L1K-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 27-Jun-14 A | 29-Sep-14 A | |
| LL1-Z3-6009 | Frame Ceilings [DELETED] | 4 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1B-6016 | Electrical RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| L1B-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| LL1-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-Z2-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L1B-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-6024 | Inspections for Cover | 1 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L1B-6020 | Hollow Metal Door Frames | 5 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| LL1-Z3-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L1K-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 06-Aug-14 A | |
| LL1-Z2-6024 | Inspections for Cover | 2 | 0 | 07-Aug-14 A | 08-Aug-14 A | |
| L1K-6020 | Hollow Metal Door Frames | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-Z2-6009 | Frame Ceilings & Inspection | 6 | 0 | 22-Aug-14 A | 13-Oct-14 A | |
| L1L-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Aug-14 A | 13-Oct-14 A | |
| LL1-6009 | Frame Ceilings & Inspection (except for bar redesign | 9 | 0 | 02-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3-6024 | Inspections for Cover | 2 | 0 | 12-Sep-14 A | 12-Sep-14 A | |

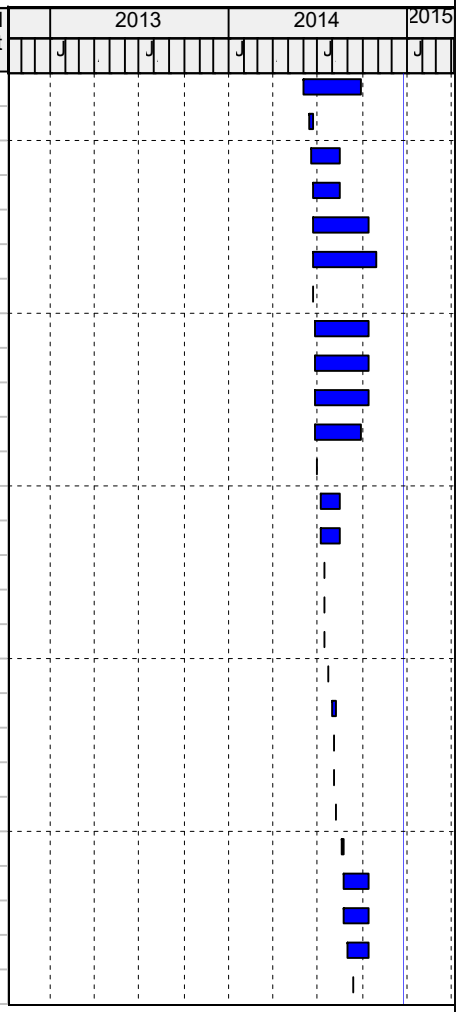


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6016 | Complete Electrical RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3C-6018 | Complete HVAC RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| L1KC-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 4 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L1B-6024 | Inspections for Cover (Main Ballroom N/S/W Walls & | 3 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1K-6024 | Inspections for Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1KC-6014 | Complete Plumbing RI @ Ceilings & Inspection | 4 | 0 | 02-Oct-14 A | 07-Oct-14 A | |
| L1BC-6014 | Complete Plumbing RI @ Ceilings | 7 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L1BC-6018 | Complete HVAC RI @ Ceilings | 7 | 0 | 06-Oct-14 A | 07-Nov-14 A | |
| L1KC-6018 | Complete HVAC RI @ Ceilings & Inspection | 4 | 0 | 06-Oct-14 A | 10-Nov-14 A | |
| L1KC-6016 | Complete Electrical RI @ Ceilings & Inspection | 3 | 0 | 20-Oct-14 A | 10-Nov-14 A | |
| L1KC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 3 | 0 | 20-Oct-14 A | 10-Nov-14 A | |
| L1L-6024 | Inspections for Cover | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L1L-6009 | Frame Ceilings & Inspection | 13 | 2 | 24-Nov-14 A | 23-Dec-14 | 8 |
| L1B-6009 | Frame Ceilings | 5 | 5 | 04-Dec-14 A | 30-Dec-14 | 5 |
| L1BC-6012 | Complete Fire Sprinkler RI @ Ceilings | 6 | 6 | 22-Dec-14 | 31-Dec-14 | 10 |
| L1K-6009 | Frame Ceilings [public restroom] | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 13 |
| L1BC-6016 | Complete Electrical RI @ Ceilings & Inspection | 6 | 6 | 31-Dec-14 | 08-Jan-15 | 5 |
| L1BC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 6 | 6 | 31-Dec-14 | 08-Jan-15 | 5 |
| L1LC-6012 | Complete Fire Sprinkler RI @ Ceilings | 4 | 4 | 06-Jan-15 | 09-Jan-15 | 2 |
| L1LC-6014 | Complete Plumbing RI @ Ceilings | 4 | 4 | 06-Jan-15 | 09-Jan-15 | 2 |
| L1LC-6016 | Complete Electrical RI @ Ceilings | 4 | 4 | 06-Jan-15 | 09-Jan-15 | 2 |
| L1LC-6018 | Complete HVAC RI @ Ceilings | 4 | 4 | 06-Jan-15 | 09-Jan-15 | 2 |
| L1LC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 4 | 4 | 06-Jan-15 | 09-Jan-15 | 2 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |

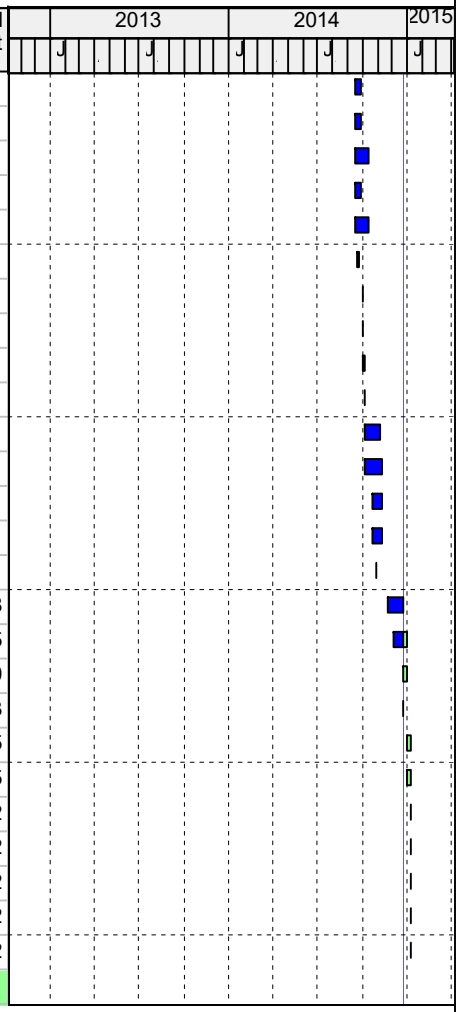



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 0 | 17-Apr-14 A | 09-May-14 A | |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6006 | L2 - Support Frame/Sheathing for Metal Panels | 6 | 0 | 23-Apr-14 A | 07-Aug-14 A | |
| L02-6008 | L2 - Int Wall Framing | 10 | 0 | 25-Apr-14 A | 17-Jul-14 A | |
| L02-6014 | L2 - Plumbing RI | 15 | 0 | 28-Apr-14 A | 07-Aug-14 A | |
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 0 | 28-Apr-14 A | 09-May-14 A | |
| L02-6004 | L2 - CMU Walls | 5 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L02-6002 | L2 - Layout | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L02-6018 | L2 - HVAC RI (including equipment) | 20 | 0 | 18-Jun-14 A | 10-Sep-14 A | |
| L02-6016 | L2 - Electrical RI | 10 | 0 | 24-Jun-14 A | 14-Aug-14 A | |
| L02-6022 | L2 - Fire Alarm / Elec Specialties RI | 10 | 0 | 24-Jun-14 A | 10-Oct-14 A | |
| L02-6012 | L2 - Fire Sprinkler RI | 10 | 0 | 26-Jun-14 A | 07-Aug-14 A | |
| L02-6020 | L2 - H Mtl Frames | 5 | 0 | 11-Jul-14 A | 17-Jul-14 A | |
| L02-6024 | L2 - Inspections - North Half | 2 | 0 | 10-Oct-14 A | 20-Oct-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L07-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 01-Apr-11 A | 11-Apr-11 A | |
| L04-6012 | Fire Sprinkler Mains | 5 | 0 | 01-Feb-14 A | 03-Apr-14 A | |
| L03-8219 | HVAC Risers | 5 | 0 | 11-Feb-14 A | 23-Mar-14 A | |
| L03-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 11-Feb-14 A | 03-Mar-14 A | |
| L03-6002 | Layout | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| L04-8219 | HVAC Risers | 5 | 0 | 13-Feb-14 A | 23-Mar-14 A | |
| L05-8219 | HVAC Risers | 5 | 0 | 17-Feb-14 A | 03-Mar-14 A | |
| L03-6008 | Frame Shaft Walls | 3 | 0 | 18-Feb-14 A | 26-Mar-14 A | |
| L04-6002 | Layout | 5 | 0 | 19-Feb-14 A | 25-Feb-14 A | |
| L04-6008 | Frame Shaft Walls | 3 | 0 | 20-Feb-14 A | 26-Mar-14 A | |

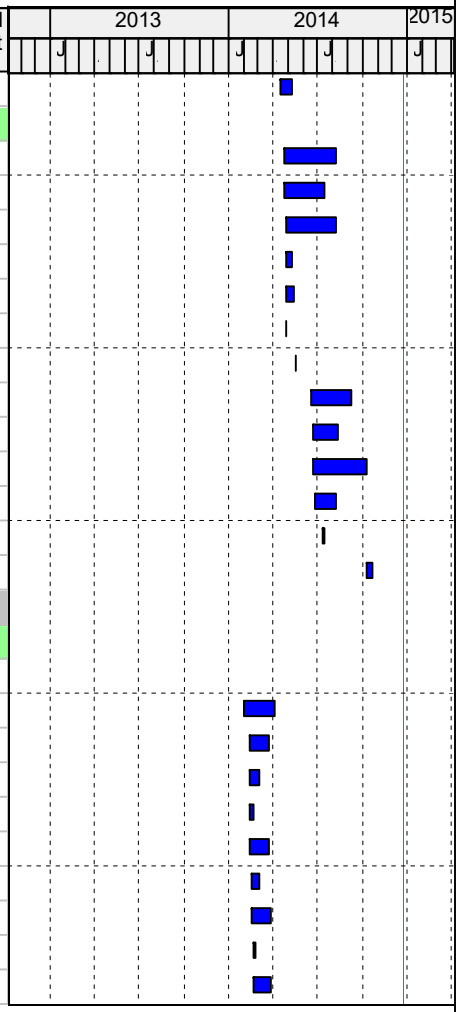



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6011 | PreRock Shafts | 2 | 0 | 24-Feb-14 A | 25-Mar-14 A | |
| L03-6010 | Frame Walls | 5 | 0 | 25-Feb-14 A | 25-Mar-14 A | |
| L05-6002 | Layout | 5 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| L04-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 28-Feb-14 A | 05-Mar-14 A | |
| L03-6016 | Electrical RI | 5 | 0 | 03-Mar-14 A | 04-Apr-14 A | |
| L03-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 12-Mar-14 A | |
| L04-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 13-Mar-14 A | |
| L04-6010 | Frame Walls | 5 | 0 | 04-Mar-14 A | 05-Jun-14 A | |
| L05-6008 | Frame Shaft Walls | 3 | 0 | 05-Mar-14 A | 27-Mar-14 A | |
| L06-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L07-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L05-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 06-Mar-14 A | 21-Mar-14 A | |
| L03-6020 | Install Hollow Metal Frames | 3 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L04-6020 | Install Hollow Metal Frames | 3 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L05-6010 | Frame Walls | 5 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L06-6002 | Layout | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L04-6011 | PreRock Shafts | 2 | 0 | 18-Mar-14 A | 25-Mar-14 A | |
| L05-6009 | Inspect Shafts | 1 | 0 | 18-Mar-14 A | 18-Mar-14 A | |
| L05-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| L06-6008 | Frame Shaft Walls | 3 | 0 | 19-Mar-14 A | 03-Apr-14 A | |
| L06-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 27-Mar-14 A | |
| L04-6016 | Electrical RI | 5 | 0 | 20-Mar-14 A | 09-Apr-14 A | |
| L05-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 26-Mar-14 A | |
| L06-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 07-Apr-14 A | |
| L07-6002 | Layout | 5 | 0 | 24-Mar-14 A | 30-Apr-14 A | |
| L03-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L03-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |

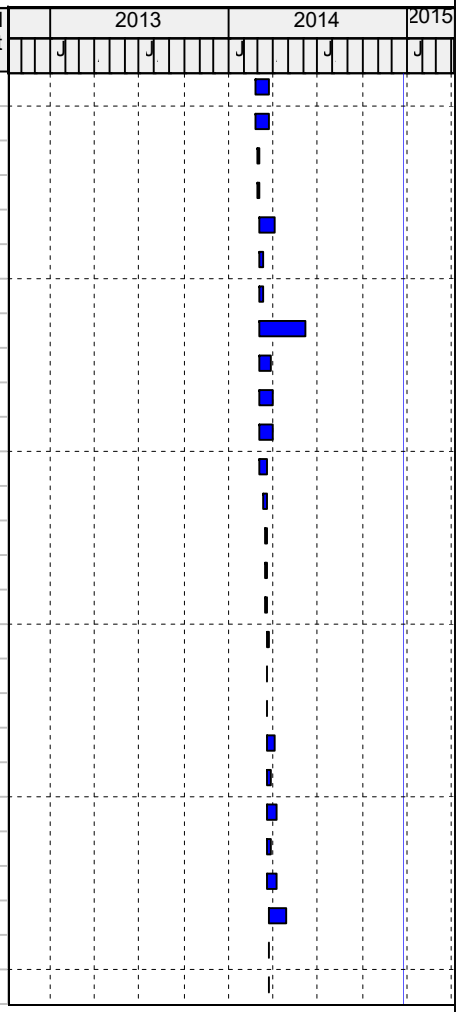


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L05-6016 | Electrical RI | 5 | 0 | 25-Mar-14 A | 05-Jun-14 A | |
| L04-6019 | Complete Top Out GWB | 2 | 0 | 26-Mar-14 A | 06-Jun-14 A | |
| L05-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L06-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| L03-6019 | Complete Top Out GWB | 2 | 0 | 27-Mar-14 A | 02-May-14 A | |
| L08-6002 | Layout | 5 | 0 | 27-Mar-14 A | 02-Apr-14 A | |
| L05-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 28-Mar-14 A | 03-Apr-14 A | |
| L06-6010 | Frame Walls | 5 | 0 | 28-Mar-14 A | 07-Apr-14 A | |
| L03-6012 | Fire Sprinkler Mains | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L07-6008 | Frame Shaft Walls | 3 | 0 | 31-Mar-14 A | 03-Apr-14 A | |
| L05-6019 | Complete Top Out GWB | 2 | 0 | 01-Apr-14 A | 08-Apr-14 A | |
| L08-6008 | Frame Shaft Walls | 3 | 0 | 02-Apr-14 A | 21-Apr-14 A | |
| L03-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L04-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L05-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L06-6016 | Electrical RI | 5 | 0 | 03-Apr-14 A | 15-Apr-14 A | |
| L07-6009 | Inspect Shafts | 1 | 0 | 03-Apr-14 A | 03-Apr-14 A | |
| L07-6011 | PreRock Shafts | 2 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| L05-6012 | Fire Sprinkler Mains | 5 | 0 | 04-Apr-14 A | 30-Apr-14 A | |
| L06-6012 | Fire Sprinkler Mains | 5 | 0 | 07-Apr-14 A | 30-Apr-14 A | |
| L06-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L06-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L07-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| L07-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L03-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |

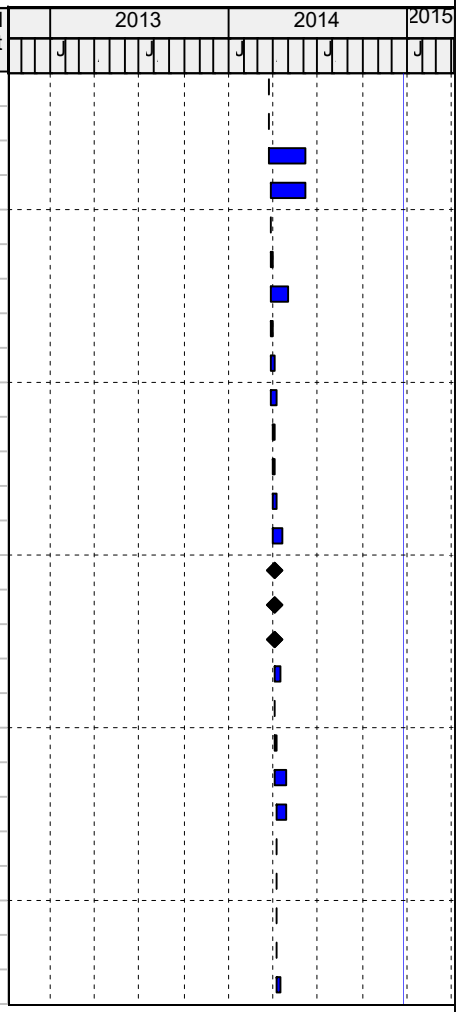


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L04-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L06-6009 | Inspect Shafts | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L06-6019 | Complete Top Out GWB | 2 | 0 | 08-Apr-14 A | 18-Apr-14 A | |
| L07-6010 | Frame Walls | 5 | 0 | 08-Apr-14 A | 15-Apr-14 A | |
| L08-6011 | PreRock Shafts | 2 | 0 | 08-Apr-14 A | 23-Apr-14 A | |
| L09-6002 | Layout | 5 | 0 | 08-Apr-14 A | 26-Apr-14 A | |
| L03-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 09-Apr-14 A | 08-May-14 A | |
| L03-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L05-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 09-Apr-14 A | 14-Apr-14 A | |
| L08-6009 | Inspect Shafts | 1 | 0 | 09-Apr-14 A | 25-Apr-14 A | |
| L09-6008 | Frame Shaft Walls | 3 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| L08-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| L04-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 15-Apr-14 A | 16-Apr-14 A | |
| L07-6012 | Fire Sprinkler Mains | 5 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| L07-6016 | Electrical RI | 5 | 0 | 15-Apr-14 A | 12-May-14 A | |
| L07-6020 | Install Hollow Metal Frames | 3 | 0 | 16-Apr-14 A | 23-Apr-14 A | |
| L05-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 17-Apr-14 A | 25-Apr-14 A | |
| L06-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 17-Apr-14 A | 12-May-14 A | |
| L06-6023 | Inspection of Exterior Framing | 0 | 0 | 17-Apr-14 A | | |
| L09-8219 | HVAC Risers | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L09-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L04-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 18-Apr-14 A | 20-Apr-14 A | |
| L04-6028 | PreRock at Heat Pumps | 2 | 0 | 20-Apr-14 A | 22-Apr-14 A | |
| L08-8219 | HVAC Risers | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |

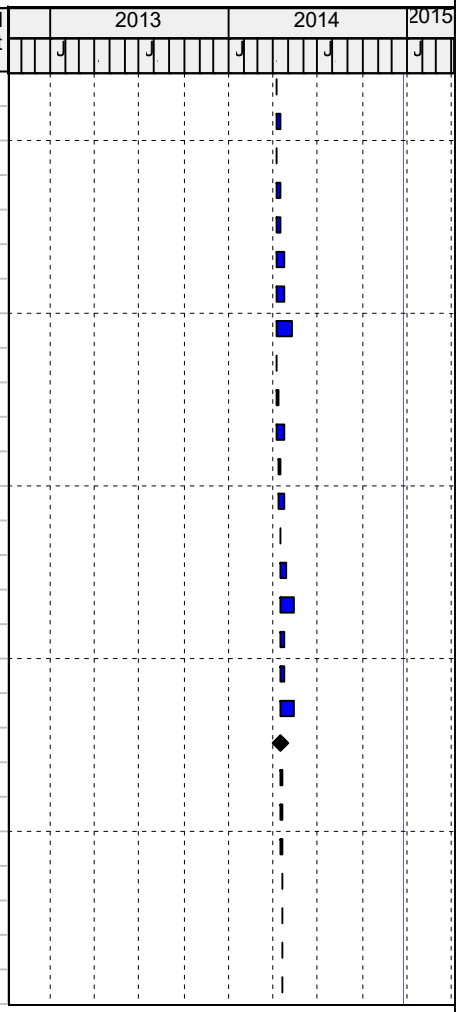


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6009 | Inspect Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6011 | PreRock Shafts | 2 | 0 | 22-Apr-14 A | 24-Apr-14 A | |
| L04-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L06-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 23-Apr-14 A | 25-Apr-14 A | |
| L08-6020 | Install Hollow Metal Frames | 3 | 0 | 23-Apr-14 A | 13-May-14 A | |
| L11-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L11-8220 | Plumbing Risers - Install | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L04-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L09-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L10-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L10-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 20-May-14 A | |
| L12-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L04-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 25-Apr-14 A | 11-Jun-14 A | |
| L04-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L09-6010 | Frame Walls | 5 | 0 | 25-Apr-14 A | 20-May-14 A | |
| L09-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L10-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L11-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 30-Apr-14 A | |
| L12-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L08-6010 | Frame Walls | 5 | 0 | 26-Apr-14 A | 30-Apr-14 A | |
| L10-6002 | Layout | 5 | 0 | 27-Apr-14 A | 27-Apr-14 A | |
| L04-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 28-Apr-14 A | 30-Apr-14 A | |
| L05-6018 | HVAC RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6028 | PreRock at Heat Pumps | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |

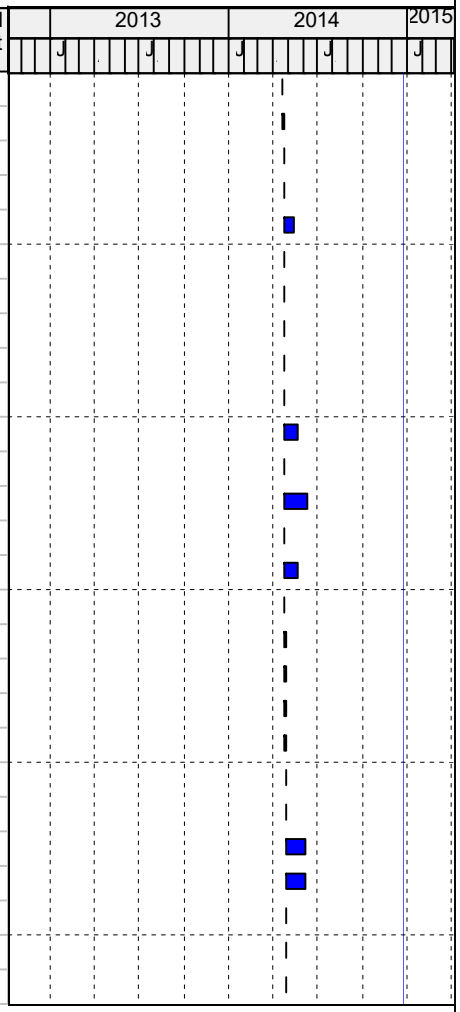



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 28-Apr-14 A | 12-May-14 A | |
| L10-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-Apr-14 A | 22-May-14 A | |
| L11-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L12-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L05-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| L05-6028 | PreRock at Heat Pumps | 2 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L06-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 09-May-14 A | |
| L06-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L06-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L08-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L08-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L09-6020 | Install Hollow Metal Frames | 3 | 0 | 29-Apr-14 A | 20-May-14 A | |
| L09-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L10-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L04-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 30-Apr-14 A | 02-May-14 A | |
| L09-6019 | Complete Top Out GWB | 2 | 0 | 30-Apr-14 A | 06-Jun-14 A | |
| L11-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L12-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L03-6028 | PreRock at Heat Pumps | 2 | 0 | 01-May-14 A | 02-May-14 A | |
| L05-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L06-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L03-6014 | Set Tubs & Plumbing RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |

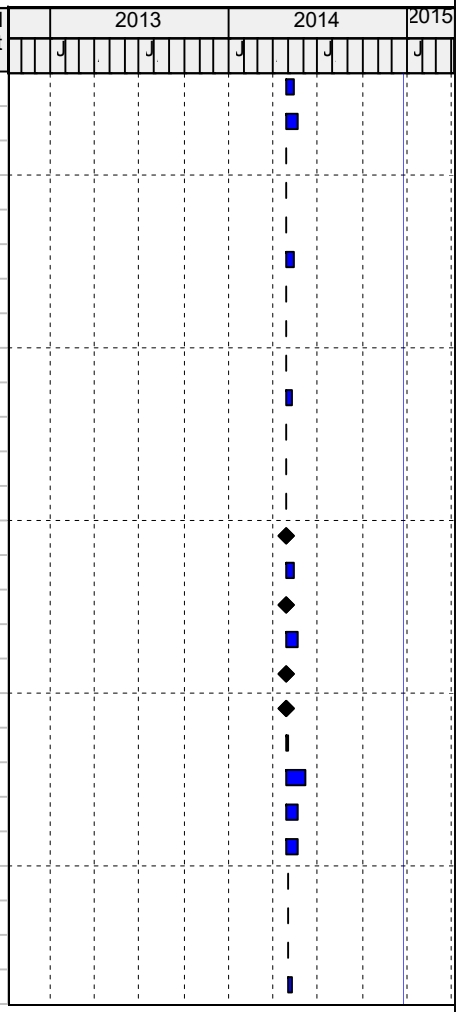


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L05-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L05-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| L06-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L06-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 09-May-14 A | |
| L03-6018 | HVAC Rl | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L03-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 06-May-14 A | 06-May-14 A | |
| L07-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L07-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 06-May-14 A | 09-May-14 A | |
| L03-6004 | CMU Wall/Clips | 3 | 0 | 07-May-14 A | 08-May-14 A | |
| L03-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L03-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 08-May-14 A | 13-May-14 A | |
| L03-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6004 | CMU Walls | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6018 | HVAC Rl | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L11-6010 | Frame Walls | 5 | 0 | 09-May-14 A | 15-May-14 A | |
| L05-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 12-May-14 A | 05-Jun-14 A | |
| L07-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 0 | 12-May-14 A | 13-May-14 A | |
| L11-6020 | Install Hollow Metal Frames | 3 | 0 | 12-May-14 A | 14-May-14 A | |
| L11-6019 | Complete Top Out GWB | 2 | 0 | 12-May-14 A | 14-May-14 A | |
| L14-6002 | Layout | 5 | 0 | 12-May-14 A | 14-May-14 A | |
| L15-6002 | Layout | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L05-6004 | CMU Walls | 3 | 0 | 13-May-14 A | 13-May-14 A | |

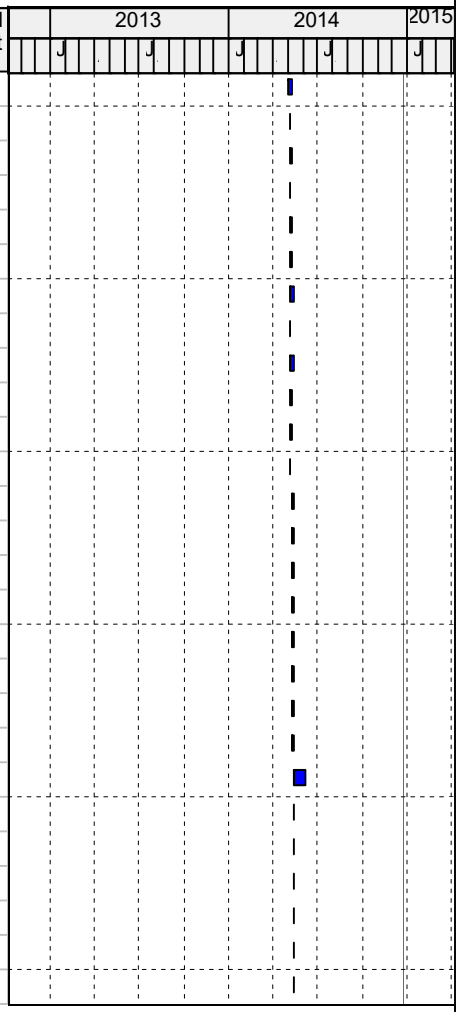


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 25-Jun-14 A | |
| L06-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 13-May-14 A | 14-Jul-14 A | |
| L07-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 05-Jun-14 A | |
| L07-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| L07-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 13-May-14 A | 13-May-14 A | |
| L14-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L16-6002 | Layout | 5 | 0 | 13-May-14 A | 16-May-14 A | |
| L06-6004 | CMU Walls | 3 | 0 | 14-May-14 A | 14-May-14 A | |
| L07-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 15-May-14 A | |
| L08-6012 | Fire Sprinkler Mains | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6002 | Layout | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L07-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6014 | Set Tubs & Plumbing RI | 5 | 0 | 16-May-14 A | 25-Jun-14 A | |
| L08-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L11-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L12-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L07-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L08-6028 | PreRock at Heat Pumps | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L09-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L10-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L11-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L15-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 19-May-14 A | 19-May-14 A | |
| L07-6028 | PreRock at Heat Pumps | 2 | 0 | 20-May-14 A | 21-May-14 A | |

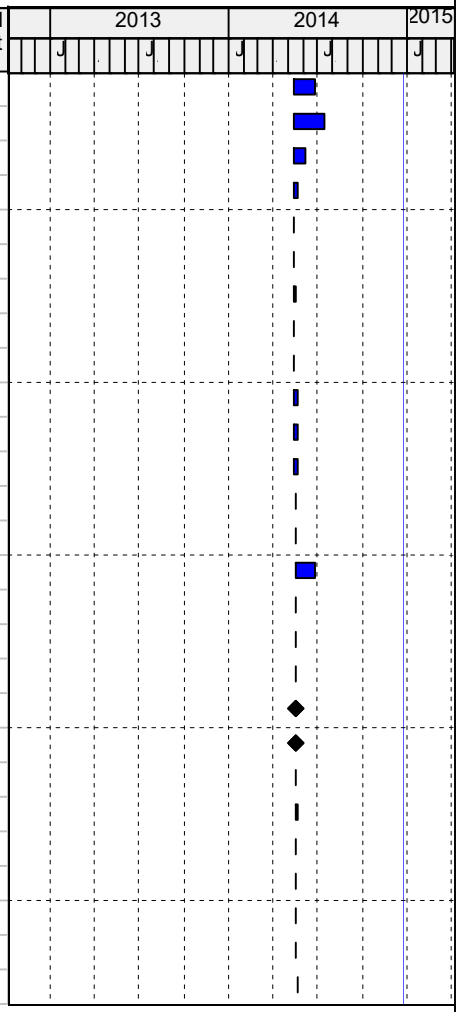


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L08-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 20-May-14 A | 21-May-14 A | |
| L10-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L11-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L14-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L07-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 21-May-14 A | 27-May-14 A | |
| L08-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L08-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L09-6028 | PreRock at Heat Pumps | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L10-6014 | Set Tubs & Plumbing RI | 5 | 0 | 21-May-14 A | 27-Jun-14 A | |
| L10-6010 | Frame Walls | 5 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6019 | Complete Top Out GWB | 2 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L11-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L12-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L14-8220 | Plumbing Risers - Install | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L15-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L16-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L07-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| L08-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 22-May-14 A | 22-May-14 A | |
| L10-6012 | Fire Sprinkler Mains | 5 | 0 | 22-May-14 A | 27-May-14 A | |
| L08-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L09-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6020 | Install Hollow Metal Frames | 3 | 0 | 23-May-14 A | 03-Jun-14 A | |
| L10-6028 | PreRock at Heat Pumps | 2 | 0 | 23-May-14 A | 27-May-14 A | |

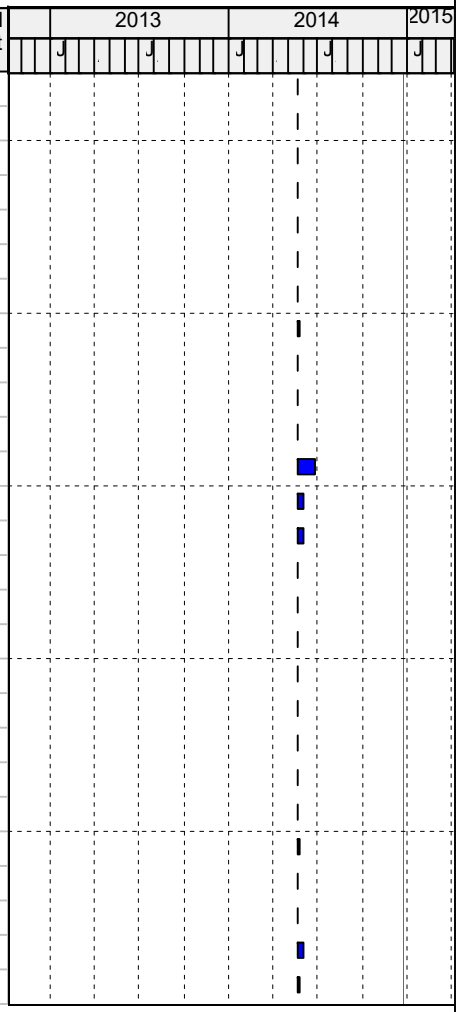



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L15-8220 | Plumbing Risers - Install | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L09-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 27-May-14 A | 27-May-14 A | |
| L12-6010 | Frame Walls | 5 | 0 | 27-May-14 A | 02-Jun-14 A | |
| L08-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L09-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 28-May-14 A | 28-May-14 A | |
| L10-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 28-May-14 A | 03-Jun-14 A | |
| L14-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L15-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-May-14 A | 30-May-14 A | |
| L16-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 28-May-14 A | 28-May-14 A | |
| L16-8220 | Plumbing Risers - Install | 2 | 0 | 28-May-14 A | 29-May-14 A | |
| L08-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 29-May-14 A | 30-May-14 A | |
| L10-6016 | Electrical RI | 5 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L10-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| L12-6012 | Fire Sprinkler Mains | 5 | 0 | 30-May-14 A | 26-Jun-14 A | |
| L12-6020 | Install Hollow Metal Frames | 3 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L15-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L17-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L17-8220 | Plumbing Risers - Install | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L10-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L11-6016 | Electrical RI | 5 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L11-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L12-6019 | Complete Top Out GWB | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L14-6020 | Install Hollow Metal Frames | 3 | 0 | 02-Jun-14 A | 05-Jun-14 A | |
| L14-6010 | Frame Walls | 5 | 0 | 02-Jun-14 A | 04-Jun-14 A | |

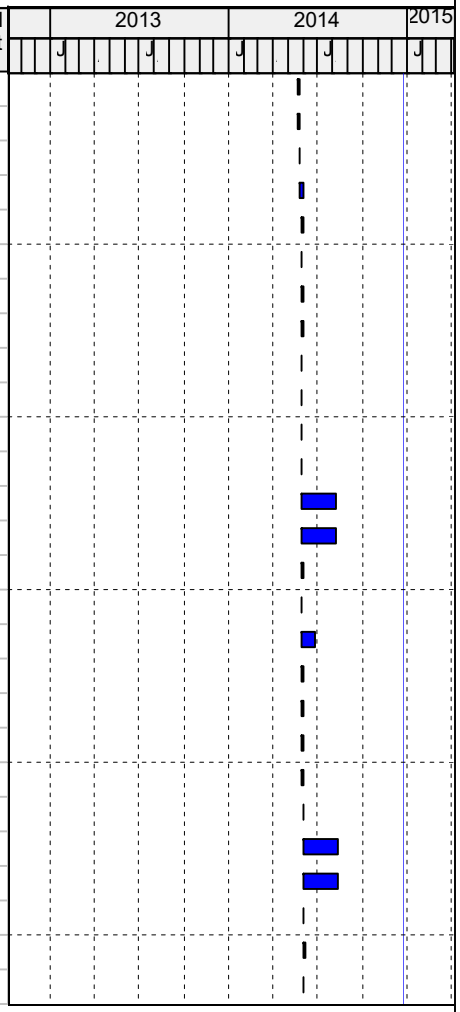



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| L14-6019 | Complete Top Out GWB | 2 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L16-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L10-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| L17-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 04-Jun-14 A | 11-Jun-14 A | |
| L08-6016 | Electrical RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L08-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L09-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L12-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L15-6010 | Frame Walls | 3 | 0 | 05-Jun-14 A | 11-Jun-14 A | |
| L09-6012 | Fire Sprinkler Mains | 5 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L09-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L11-6012 | Fire Sprinkler Mains | 4 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L12-6014 | Set Tubs & Plumbing RI | 4 | 0 | 06-Jun-14 A | 27-Jun-14 A | |
| L11-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jun-14 A | 11-Jun-14 A | |
| L09-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-Jun-14 A | 25-Jun-14 A | |
| L14-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L15-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L16-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L09-6016 | Electrical RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L14-6014 | Set Tubs & Plumbing RI | 4 | 0 | 10-Jun-14 A | 21-Jul-14 A | |
| L15-6020 | Install Hollow Metal Frames | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L15-6019 | Complete Top Out GWB | 2 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6014 | Set Tubs & Plumbing RI | 4 | 0 | 11-Jun-14 A | 26-Jun-14 A | |

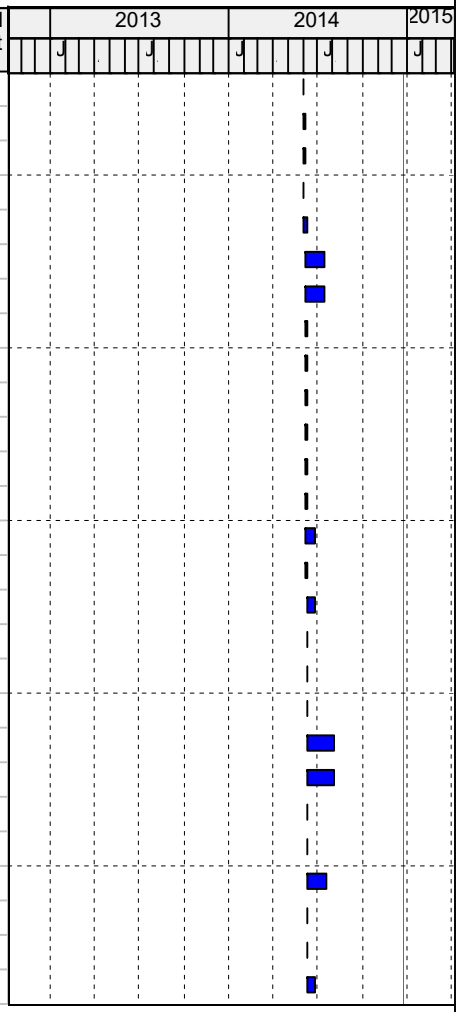



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6028 | PreRock at Heat Pumps | 2 | 0 | 13-Jun-14 A | 14-Jun-14 A | |
| L11-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 14-Jun-14 A | 14-Jun-14 A | |
| L14-6012 | Fire Sprinkler Mains | 2 | 0 | 16-Jun-14 A | 27-Jun-14 A | |
| L14-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 18-Jun-14 A | 18-Jun-14 A | |
| L15-6023 | Inspection of Exterior Framing | 0 | 0 | 18-Jun-14 A | | |
| L17-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 18-Jun-14 A | 23-Jun-14 A | |
| L17-6010 | Frame Walls | 5 | 0 | 18-Jun-14 A | 29-Jul-14 A | |
| L10-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L12-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6023 | Inspection of Exterior Framing | 0 | 0 | 20-Jun-14 A | | |
| L15-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-Jun-14 A | 20-Jun-14 A | |
| L10-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-Jun-14 A | 23-Jun-14 A | |
| L15-6014 | Set Tubs & Plumbing RI | 5 | 0 | 22-Jun-14 A | 24-Jul-14 A | |
| L08-6018 | HVAC RI | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L12-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L14-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L15-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L08-6221 | Frame Unit Ceilings | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| L11-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 24-Jun-14 A | 27-Jun-14 A | |
| L12-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L14-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6023 | Inspection of Exterior Framing | 0 | 0 | 24-Jun-14 A | | |
| L12-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| L12-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |

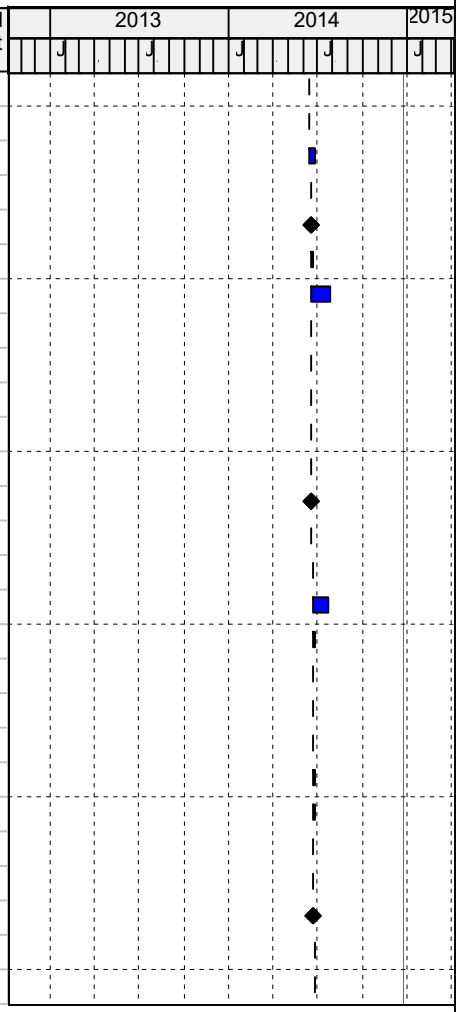


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L15-6012 | Fire Sprinkler Mains | 2 | 0 | 25-Jun-14 A | 22-Jul-14 A | |
| L16-6023 | Inspection of Exterior Framing | 0 | 0 | 25-Jun-14 A | | |
| L03-6024 | Inspections for GWB Cover | 1 | 0 | 27-Jun-14 A | 27-Jun-14 A | |
| L09-6018 | HVAC RI | 3 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L09-6221 | Frame Unit Ceilings | 2 | 0 | 27-Jun-14 A | 30-Jun-14 A | |
| L12-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L14-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L15-6028 | PreRock at Heat Pumps | 2 | 0 | 30-Jun-14 A | 01-Jul-14 A | |
| L16-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 30-Jun-14 A | 30-Jun-14 A | |
| L16-6010 | Frame Walls | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| L16-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L15-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L15-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L04-6024 | Inspections for GWB Cover | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L10-6018 | HVAC RI | 3 | 0 | 07-Jul-14 A | 21-Jul-14 A | |
| L11-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L15-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L16-6012 | Fire Sprinkler Mains | 2 | 0 | 07-Jul-14 A | 24-Jul-14 A | |
| L16-6020 | Install Hollow Metal Frames | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L16-6028 | PreRock at Heat Pumps | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L17-6019 | Complete Top Out GWB | 1 | 0 | 07-Jul-14 A | 08-Aug-14 A | |
| L11-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L15-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 08-Jul-14 A | 04-Aug-14 A | |
| L17-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jul-14 A | 01-Aug-14 A | |
| L10-6221 | Frame Unit Ceilings | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| L17-6012 | Fire Sprinkler Mains | 2 | 0 | 09-Jul-14 A | 12-Aug-14 A | |

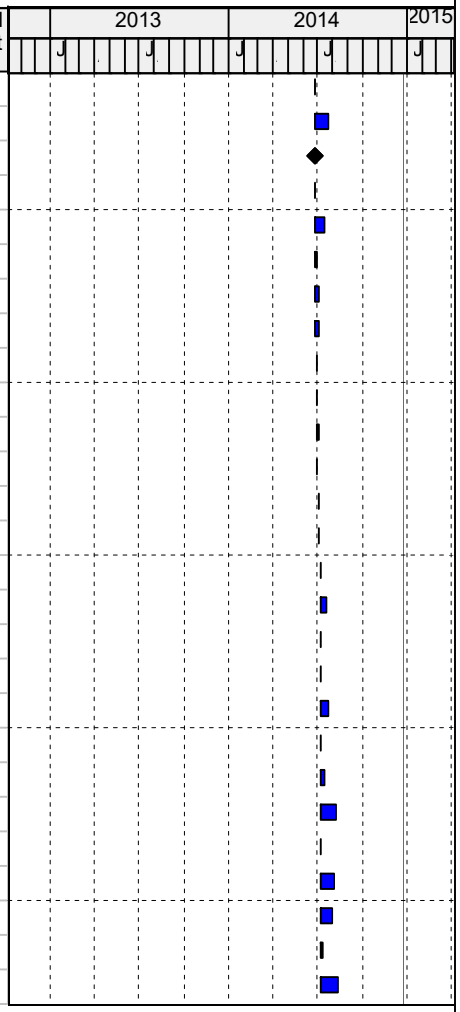



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6024 | Inspections for GWB Cover | 2 | 0 | 10-Jul-14 A | 10-Jul-14 A | |
| L04-6000 | Tape/Finish GWB | 6 | 0 | 11-Jul-14 A | 23-Jul-14 A | |
| L16-6019 | Complete Top Out GWB | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L16-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L15-6018 | HVAC RI | 3 | 0 | 16-Jul-14 A | 18-Jul-14 A | |
| L16-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-6024 | Inspections for GWB Cover | 2 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6018 | HVAC RI | 3 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L16-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 21-Jul-14 A | 18-Aug-14 A | |
| L15-6013 | Fire Sprinkler Branch Lines | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| L03-6000 | Tape/Finish GWB | 6 | 0 | 23-Jul-14 A | 29-Jul-14 A | |
| L11-6018 | HVAC RI | 3 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L15-6221 | Frame Unit Ceilings | 2 | 0 | 23-Jul-14 A | 01-Aug-14 A | |
| L16-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L17-6020 | Install Hollow Metal Frames | 3 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| L11-6221 | Frame Unit Ceilings | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L12-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L14-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L14-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L16-6014 | Set Tubs & Plumbing RI | 5 | 0 | 28-Jul-14 A | 18-Aug-14 A | |
| L07-6024 | Inspections for GWB Cover | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L12-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |

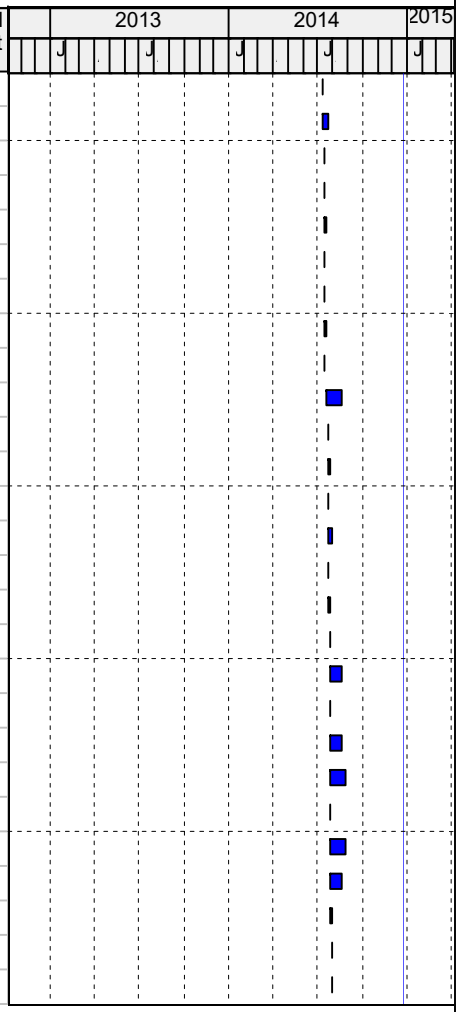



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6000 | Tape/Finish GWB | 6 | 0 | 31-Jul-14 A | 05-Aug-14 A | |
| L08-6024 | Inspections for GWB Cover | 2 | 0 | 31-Jul-14 A | 31-Jul-14 A | |
| L12-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L14-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L06-6000 | Tape/Finish GWB | 4 | 0 | 06-Aug-14 A | 11-Aug-14 A | |
| L09-6024 | Inspections for GWB Cover | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L07-6000 | Tape/Finish GWB | 5 | 0 | 07-Aug-14 A | 16-Aug-14 A | |
| L11-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 08-Aug-14 A | 14-Aug-14 A | |
| L17-6014 | Set Tubs & Plumbing RI | 5 | 0 | 08-Aug-14 A | 16-Sep-14 A | |
| L10-6024 | Inspections for GWB Cover | 2 | 0 | 11-Aug-14 A | 12-Aug-14 A | |
| L09-6000 | Tape/Finish GWB | 5 | 0 | 14-Aug-14 A | 19-Aug-14 A | |
| L08-6000 | Tape/Finish GWB | 5 | 0 | 16-Aug-14 A | 21-Aug-14 A | |
| L11-6024 | Inspections for GWB Cover | 2 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L16-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 18-Aug-14 A | 29-Aug-14 A | |
| L10-6000 | Tape/Finish GWB | 5 | 0 | 19-Aug-14 A | 23-Aug-14 A | |
| L16-6221 | Frame Unit Ceilings | 4 | 0 | 21-Aug-14 A | 26-Aug-14 A | |
| L17-6018 | HVAC RI | 3 | 0 | 21-Aug-14 A | 10-Sep-14 A | |
| L12-6024 | Inspections for GWB Cover | 2 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L15-6016 | Electrical RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L15-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L11-6000 | Tape/Finish GWB | 5 | 0 | 23-Aug-14 A | 29-Aug-14 A | |
| L17-6221 | Frame Unit Ceilings | 4 | 0 | 26-Aug-14 A | 28-Aug-14 A | |
| L14-6024 | Inspections for GWB Cover | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L16-6016 | Electrical RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L16-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |

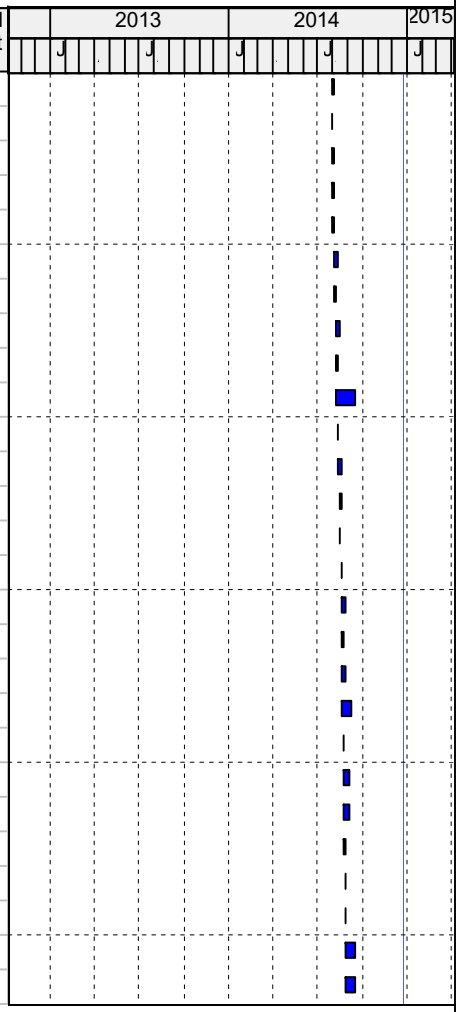



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-6000 | Tape/Finish GWB | 5 | 0 | 02-Sep-14 A | 08-Sep-14 A | |
| L15-6024 | Inspections for GWB Cover | 2 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L14-6000 | Tape/Finish GWB | 5 | 0 | 06-Sep-14 A | 11-Sep-14 A | |
| L15-6000 | Tape/Finish GWB | 4 | 0 | 12-Sep-14 A | 20-Sep-14 A | |
| L17-6016 | Electrical Rl | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-6028 | PreRock at Heat Pumps | 2 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L17-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L17-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L17-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 24-Sep-14 A | 27-Sep-14 A | |
| L17-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L16-6024 | Inspections for GWB Cover | 1 | 0 | 08-Oct-14 A | 09-Oct-14 A | |
| L16-6000 | Tape/Finish GWB | 4 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6024 | Inspections for GWB Cover | 1 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6000 | Tape/Finish GWB | 6 | 0 | 30-Oct-14 A | 07-Nov-14 A | |
| **Mechanical Penthouse** | | | | | | |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 0 | 11-Jun-14 A | 20-Jun-14 A | |
| PH-6006 | PH - Exterior Wall Framing (including PH roof parapet | 6 | 0 | 12-Jun-14 A | 14-Jul-14 A | |
| PH-6014 | PH - Plumbing/Piping Rl | 40 | 0 | 25-Jun-14 A | 05-Nov-14 A | |
| PH-6002 | PH - Layout | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| PH-6008 | PH - Interior Wall Framing | 3 | 0 | 24-Jul-14 A | 08-Aug-14 A | |
| PH-6020 | PH - H Mtl Frames | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| PH-6012 | PH - Fire Sprinkler Rl | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |
| PH-6018 | PH - HVAC Rl | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |

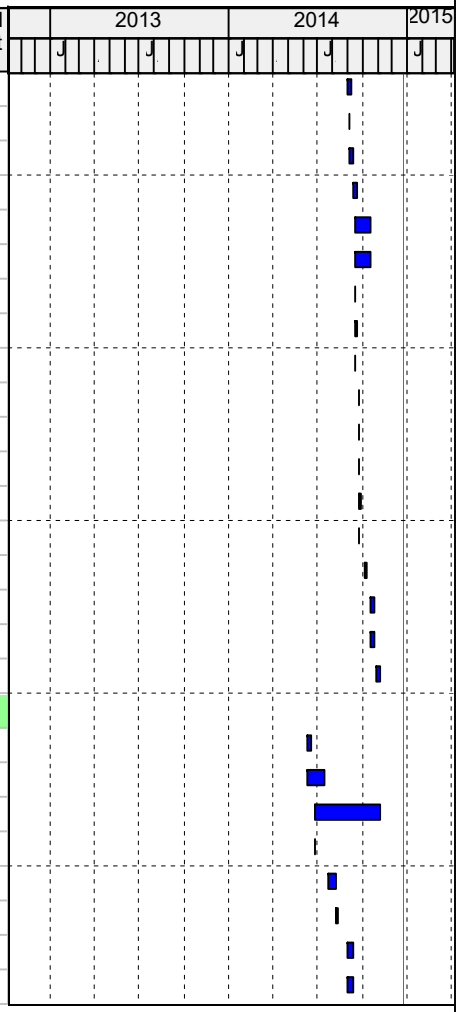



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-6016 | PH - Electrical RI | 10 | 0 | 23-Sep-14 A | 14-Nov-14 A | |
| PH-6022 | PH - Fire Alarm / Elec Specialties RI | 10 | 0 | 23-Sep-14 A | 14-Nov-14 A | |
| **Finishes** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL4-8100 | LL4 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| LL4-8102 | LL4 - GWB Hang (incl. screw inspection) | 3 | 0 | 27-Oct-14 A | 10-Dec-14 A | |
| LL4-8104 | LL4 - Int Painting | 1 | 1 | 22-Dec-14 | 22-Dec-14 | 37 |
| LL4-8122 | LL4 - Plumbing Trim / Finish | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 48 |
| LL4-8108 | LL4 - Elec Trim / Finish | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 48 |
| LL4-8110 | LL4 - HVAC Trim / Finish | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 48 |
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 44 |
| LL4-8118 | LL4 - Elec Specialties Trim / Finish | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 37 |
| LL4-8124 | LL4 - Flooring (VCT) | 3 | 3 | 31-Dec-14 | 05-Jan-15 | 48 |
| LL4-8126 | LL4 - Doors & Hardware | 2 | 2 | 06-Jan-15 | 07-Jan-15 | 48 |
| LL4-8114 | LL4 - Striping / Signage | 5 | 5 | 07-Jan-15 | 13-Jan-15 | 48 |
| LL4-8132 | LL4 - Punch | 3 | 3 | 13-Jan-15 | 15-Jan-15 | 48 |
| LL4-8134 | LL4 - Clean | 3 | 3 | 13-Jan-15 | 15-Jan-15 | 48 |
| LL4-8214 | LL4 - Floor Complete | 0 | 0 | | 15-Jan-15 | 48 |
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL3-8100 | LL3 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| LL3-8102 | LL3 - GWB Hang (incl. screw inspection) | 3 | 0 | 27-Oct-14 A | 10-Dec-14 A | |
| LL3-8104 | LL3 - Int Painting | 1 | 1 | 22-Dec-14 | 22-Dec-14 | 37 |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 48 |
| LL3-8108 | LL3 - Elec Trim / Finish | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 48 |

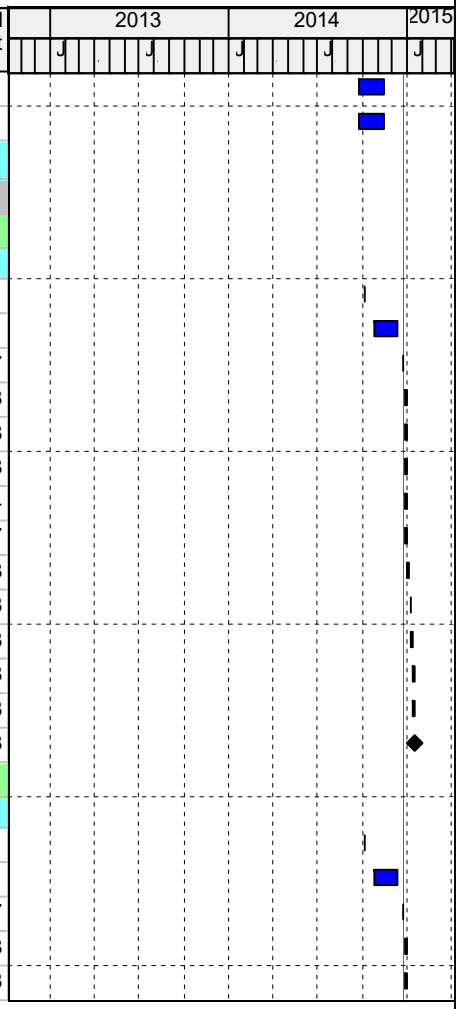



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-8110 | LL3 - HVAC Trim / Finish | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 48 |
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 44 |
| LL3-8118 | LL3 - Elec Specialties Trim / Finish | 2 | 2 | 29-Dec-14 | 30-Dec-14 | 37 |
| LL3-8124 | LL3 - Flooring (VCT) | 3 | 3 | 31-Dec-14 | 05-Jan-15 | 48 |
| LL3-8126 | LL3 - Doors & Hardware | 2 | 2 | 06-Jan-15 | 07-Jan-15 | 48 |
| LL3-8114 | LL3 - Striping / Signage | 5 | 5 | 07-Jan-15 | 13-Jan-15 | 48 |
| LL3-8132 | LL3 - Punch | 3 | 3 | 13-Jan-15 | 15-Jan-15 | 48 |
| LL3-8134 | LL3 - Clean | 3 | 3 | 13-Jan-15 | 15-Jan-15 | 48 |
| LL3-8214 | LL3 - Floor Complete | 0 | 0 | | 15-Jan-15 | 48 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL2E-8102 | LL2 - GWB Hang / Tape / Finish @ Electrical Rooms | 8 | 0 | 24-Jun-14 A | 03-Jul-14 A | |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish & Inspection | 6 | 1 | 16-Sep-14 A | 22-Dec-14 | 39 |
| LL2-8100 | LL2 - Insulation | 5 | 0 | 16-Sep-14 A | 09-Oct-14 A | |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 5 | 0 | 17-Sep-14 A | 27-Oct-14 A | |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| LL2-8104 | LL2 - Int Painting | 5 | 1 | 25-Nov-14 A | 23-Dec-14 | 31 |
| LL2-8136 | LL2 - Chainlink Fencing / Gate @ Recycling | 3 | 3 | 22-Dec-14 | 24-Dec-14 | 45 |
| LL2-8124 | LL2 - Flooring | 5 | 5 | 24-Dec-14 | 02-Jan-15 | 31 |
| LL2-8128 | LL2 - Entry Gates | 3 | 3 | 30-Dec-14 | 02-Jan-15 | 44 |
| LL2-8122 | LL2 - Plumbing Trim / Finish | 3 | 3 | 05-Jan-15 | 07-Jan-15 | 49 |
| LL2-8108 | LL2 - Elec Trim / Finish | 4 | 4 | 05-Jan-15 | 08-Jan-15 | 44 |
| LL2-8110 | LL2 - HVAC Trim / Finish | 3 | 3 | 05-Jan-15 | 07-Jan-15 | 45 |
| LL2-8112 | LL2 - Fire Sprinkler Trim / Finish | 2 | 2 | 05-Jan-15 | 06-Jan-15 | 40 |
| LL2-8116 | LL2 - Finish Carpentry / Millwork | 3 | 3 | 05-Jan-15 | 07-Jan-15 | 45 |
| LL2-8118 | LL2 - Elec Specialties Trim / Finish | 4 | 4 | 05-Jan-15 | 08-Jan-15 | 31 |
| LL2-8120 | LL2 - Install Bollards | 3 | 3 | 05-Jan-15 | 07-Jan-15 | 44 |

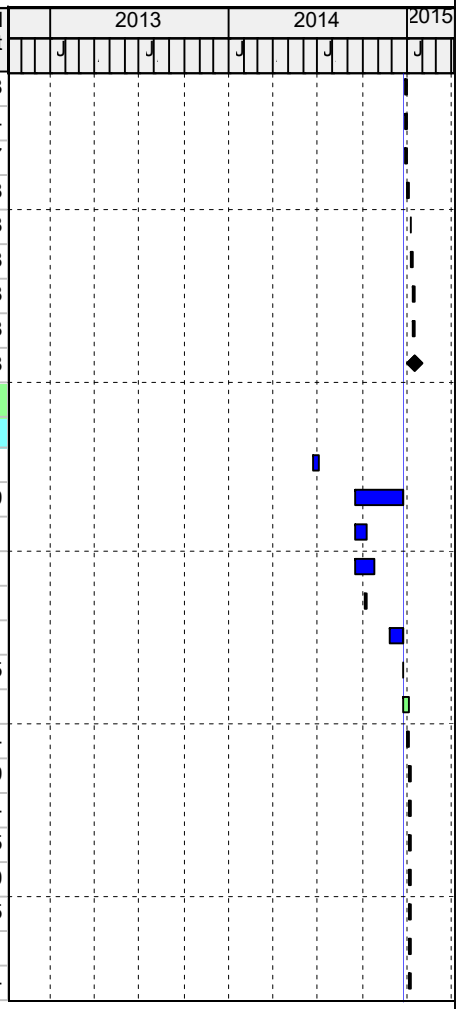



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-8114 | LL2 - Striping / Signage | 5 | 5 | 08-Jan-15 | 14-Jan-15 | 44 |
| LL2-8126 | LL2 - Doors & Hardware | 4 | 4 | 09-Jan-15 | 14-Jan-15 | 44 |
| LL2-8132 | LL2 - Punch | 5 | 5 | 23-Jan-15 | 29-Jan-15 | 38 |
| LL2-8134 | LL2 - Clean | 5 | 5 | 23-Jan-15 | 29-Jan-15 | 38 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 31-Jul-14 A | |
| LL1-Z2U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 09-May-14 A | |
| LL1-Z3U-8102 | Above Ceiling GWB (At All Areas North of Q-Line) | 5 | 0 | 10-Feb-14 A | 20-Jun-14 A | |
| L1BU-8102 | Above Ceiling GWB [including East Service Corridor] | 5 | 0 | 06-Jun-14 A | 11-Jun-14 A | |
| L1LU-8102 | Above Ceiling GWB | 5 | 0 | 24-Jun-14 A | 13-Oct-14 A | |
| L1KU-8102 | Above Ceiling GWB | 2 | 0 | 26-Jun-14 A | 22-Aug-14 A | |
| LL1-8100 | Insulation | 5 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| LL1-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 28-Jul-14 A | 06-Aug-14 A | |
| LL1-Z2-8102 | GWB Hang (Walls) & Inspection | 4 | 0 | 11-Aug-14 A | 14-Aug-14 A | |
| LL1-Z2-8100 | Insulation | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| LL1-8215 | GWB Tape (Walls) | 10 | 0 | 16-Aug-14 A | 07-Nov-14 A | |
| LL1-Z3-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 15-Sep-14 A | 07-Oct-14 A | |
| LL1-Z3-8100 | Insulation | 5 | 0 | 15-Sep-14 A | 24-Sep-14 A | |
| LL1-Z2-8215 | GWB Tape (Walls/Ceilings) | 7 | 0 | 29-Sep-14 A | 07-Nov-14 A | |
| L1B-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L1K-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| LL1-Z3-8215 | GWB Tape (Walls & Ceilings) | 7 | 0 | 07-Oct-14 A | 18-Nov-14 A | |
| L1K-8102 | GWB Hang (Walls) & Inspection | 8 | 0 | 09-Oct-14 A | 31-Oct-14 A | |
| L1L-8100 | Insulation | 4 | 0 | 13-Oct-14 A | 16-Oct-14 A | |
| L1B-8102 | GWB Hang (Walls) & Inspection - Main Ballroom N/S/ | 4 | 0 | 16-Oct-14 A | 22-Oct-14 A | |
| L1L-8102 | GWB Hang (Walls) | 4 | 2 | 30-Oct-14 A | 13-Jan-15 | 0 |

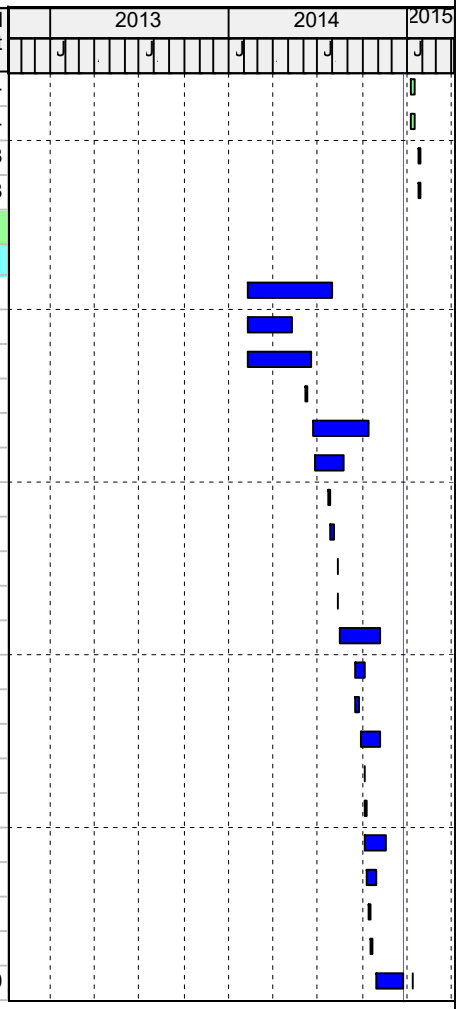


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8215 | GWB Tape (Walls & Ceilings) | 4 | 0 | 05-Nov-14 A | 18-Nov-14 A | |
| L1B-8215 | GWB Tape (Walls & Ceilings) | 4 | 3 | 06-Nov-14 A | 20-Jan-15 | 5 |
| LL1-Z3-8104 | Prime Paint | 4 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| LL1-8104 | Prime Paint & First Coat Finish Paint | 5 | 2 | 02-Dec-14 A | 23-Dec-14 | 18 |
| L1K-8114 | T Bar Grid Ceiling | 4 | 3 | 18-Dec-14 A | 24-Dec-14 | 10 |
| L1K-8106 | Wallcoverings (FRP) | 8 | 7 | 19-Dec-14 A | 02-Jan-15 | 10 |
| LL1-Z3-8114 | T Bar Grid Ceiling & Inspection | 4 | 4 | 22-Dec-14 | 29-Dec-14 | 12 |
| L1K-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 22-Dec-14 | 24-Dec-14 | 37 |
| LL1-8114 | T Bar Grid Ceiling & Inspection | 4 | 4 | 23-Dec-14 | 30-Dec-14 | 18 |
| LL1-Z2-8104 | Prime Paint | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 15 |
| LL1-Z2-8114 | T Bar Grid Ceiling & Inspection | 3 | 3 | 30-Dec-14 | 02-Jan-15 | 15 |
| LL1-Z2-8124 | Flooring | 5 | 5 | 08-Jan-15 | 14-Jan-15 | 15 |
| L1K-8104 | Prime Paint | 4 | 4 | 08-Jan-15 | 13-Jan-15 | 13 |
| LL1-Z2-8106 | Wallcoverings | 2 | 2 | 09-Jan-15 | 12-Jan-15 | 29 |
| LL1-Z3-8124 | Flooring (Epoxy) | 7 | 7 | 12-Jan-15 | 20-Jan-15 | 12 |
| L1L-8215 | GWB Hang (Ceilings) | 7 | 7 | 14-Jan-15 | 22-Jan-15 | 0 |
| LL1-Z2-8116 | Finish Carpentry / Millwork | 5 | 5 | 15-Jan-15 | 21-Jan-15 | 15 |
| LL1-8124 | Flooring | 3 | 3 | 20-Jan-15 | 22-Jan-15 | 7 |
| LL1-Z3-8116 | Finish Carpentry / Millwork | 4 | 4 | 20-Jan-15 | 23-Jan-15 | 12 |
| L1B-8104 | Prime Paint | 2 | 2 | 21-Jan-15 | 22-Jan-15 | 5 |
| LL1-Z2-8126 | Doors & Hardware | 3 | 3 | 22-Jan-15 | 26-Jan-15 | 15 |
| LL1-Z3-8126 | Doors & Hardware | 5 | 5 | 23-Jan-15 | 29-Jan-15 | 12 |
| L1B-8114 | T Bar Grid Ceiling | 2 | 2 | 23-Jan-15 | 26-Jan-15 | 5 |
| LL1-8116 | Finish Carpentry / Millwork | 5 | 5 | 26-Jan-15 | 30-Jan-15 | 7 |
| LL1-Z2-8140 | Acoustical Ceiling Tile | 2 | 2 | 27-Jan-15 | 28-Jan-15 | 15 |
| L1K-8140 | Acoustical Ceiling Tile | 4 | 4 | 27-Jan-15 | 30-Jan-15 | 10 |
| LL1-Z2-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 28-Jan-15 | 30-Jan-15 | 18 |

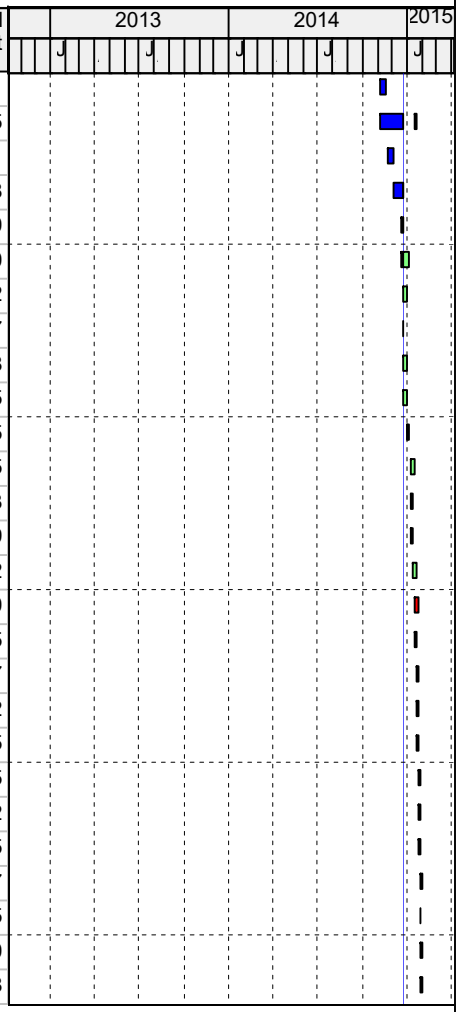



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 28-Jan-15 | 30-Jan-15 | 15 |
| L1K-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 28-Jan-15 | 30-Jan-15 | 13 |
| L1K-8124 | Flooring (VCT & Tile) | 3 | 3 | 28-Jan-15 | 30-Jan-15 | 13 |
| LL1-8126 | Doors & Hardware | 3 | 3 | 29-Jan-15 | 02-Feb-15 | 7 |
| LL1-Z3-8140 | Acoustical Ceiling Tile | 3 | 3 | 29-Jan-15 | 02-Feb-15 | 12 |
| L1B-8124 | Flooring (Carpet) | 4 | 4 | 30-Jan-15 | 04-Feb-15 | 5 |
| L1L-8104 | Prime Paint | 3 | 3 | 30-Jan-15 | 03-Feb-15 | 0 |
| LL1-Z3-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 02-Feb-15 | 04-Feb-15 | 13 |
| LL1-Z3-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 02-Feb-15 | 04-Feb-15 | 12 |
| L1K-8116 | Finish Carpentry / Millwork | 3 | 3 | 02-Feb-15 | 04-Feb-15 | 13 |
| L1K-8126 | Doors & Hardware | 3 | 3 | 02-Feb-15 | 04-Feb-15 | 13 |
| LL1-8140 | Acoustical Ceiling Tile | 3 | 3 | 03-Feb-15 | 05-Feb-15 | 7 |
| LL1-Z2-8132 | Punch | 5 | 5 | 04-Feb-15 | 10-Feb-15 | 18 |
| LL1-Z2-8134 | Clean | 5 | 5 | 04-Feb-15 | 10-Feb-15 | 18 |
| L1L-8114 | Install wood ceiling supports | 2 | 2 | 04-Feb-15 | 05-Feb-15 | 0 |
| L1B-8116 | Finish Carpentry / Millwork | 4 | 4 | 05-Feb-15 | 10-Feb-15 | 10 |
| L1B-8126 | Doors & Hardware | 4 | 4 | 05-Feb-15 | 10-Feb-15 | 9 |
| L1B-8140 | Acoustical Ceiling Tile | 4 | 4 | 05-Feb-15 | 10-Feb-15 | 5 |
| LL1-8112 | Fire Sprinkler Trim / Finish | 3 | 3 | 06-Feb-15 | 10-Feb-15 | 7 |
| LL1-8118 | Elec & Specialties Trim / Finish | 3 | 3 | 09-Feb-15 | 11-Feb-15 | 7 |
| L1L-8106 | Wallcoverings | 5 | 5 | 09-Feb-15 | 13-Feb-15 | 1 |
| L1L-8140 | Install wood ceiling | 8 | 8 | 09-Feb-15 | 18-Feb-15 | 0 |
| L1B-8112 | Fire Sprinkler Trim / Finish | 4 | 4 | 10-Feb-15 | 13-Feb-15 | 6 |
| L1B-8118 | Elec & Specialties Trim / Finish | 4 | 4 | 10-Feb-15 | 13-Feb-15 | 5 |
| L1K-8132 | Punch | 5 | 5 | 11-Feb-15 | 17-Feb-15 | 13 |
| L1K-8134 | Clean | 5 | 5 | 11-Feb-15 | 17-Feb-15 | 13 |
| LL1-Z3-8132 | Punch | 4 | 4 | 12-Feb-15 | 17-Feb-15 | 13 |

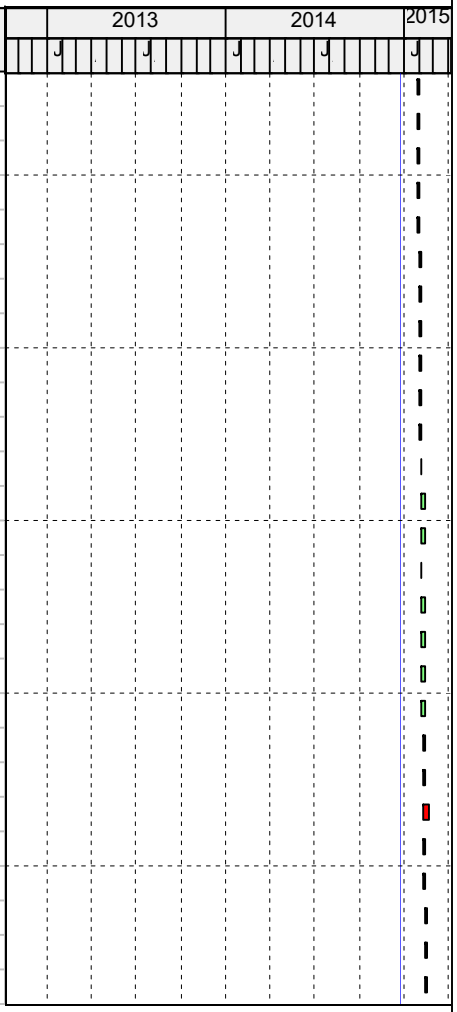



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8134 | Clean | 4 | 4 | 12-Feb-15 | 17-Feb-15 | 13 |
| L1L-8124 | Flooring | 10 | 10 | 12-Feb-15 | 25-Feb-15 | 0 |
| L1L-8116 | Finish Carpentry / Millwork | 7 | 7 | 16-Feb-15 | 24-Feb-15 | 1 |
| L1L-8126 | Doors & Hardware | 4 | 4 | 16-Feb-15 | 19-Feb-15 | 5 |
| LL1-8132 | Punch | 4 | 4 | 17-Feb-15 | 20-Feb-15 | 10 |
| LL1-8134 | Clean | 4 | 4 | 17-Feb-15 | 20-Feb-15 | 10 |
| L1L-8112 | Fire Sprinkler Trim / Finish | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 5 |
| L1L-8118 | Elec & Specialties Trim / Finish | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 2 |
| L1B-8132 | Punch | 4 | 4 | 23-Feb-15 | 26-Feb-15 | 6 |
| L1B-8134 | Clean | 4 | 4 | 23-Feb-15 | 26-Feb-15 | 6 |
| L1L-8132 | Punch | 4 | 4 | 03-Mar-15 | 06-Mar-15 | 0 |
| L1L-8134 | Clean | 4 | 4 | 03-Mar-15 | 06-Mar-15 | 0 |
| **Corridors / Common / Public Areas** | | | | | | |
| LL1-Z3-8200 | First Coat Finish Paint | 4 | 0 | 25-Nov-14 A | 03-Dec-14 A | |
| LL1-8200 | Install wall finishes | 4 | 2 | 17-Dec-14 A | 29-Dec-14 | 22 |
| LL1-Z2-8200 | First Coat Finish Paint | 3 | 3 | 06-Jan-15 | 08-Jan-15 | 15 |
| L1K-8200 | First Coat Finish Paint | 5 | 5 | 14-Jan-15 | 20-Jan-15 | 13 |
| L1B-8200 | First Coat Finish Paint | 3 | 3 | 27-Jan-15 | 29-Jan-15 | 5 |
| LL1-Z2-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 28-Jan-15 | 30-Jan-15 | 18 |
| L1K-8204 | HVAC Trim / Finish | 3 | 3 | 28-Jan-15 | 30-Jan-15 | 13 |
| LL1-Z2-8201 | Final Coat Finish Paint | 3 | 3 | 30-Jan-15 | 03-Feb-15 | 18 |
| LL1-Z3-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 02-Feb-15 | 04-Feb-15 | 13 |
| L1L-8200 | First Coat Finish Paint | 3 | 3 | 04-Feb-15 | 06-Feb-15 | 0 |
| LL1-Z3-8201 | Final Coat Finish Paint | 5 | 5 | 05-Feb-15 | 11-Feb-15 | 13 |
| L1K-8201 | Final Coat Finish Paint | 4 | 4 | 05-Feb-15 | 10-Feb-15 | 13 |
| LL1-8204 | Mech Trim / Finish (HVAC & Plumbing) | 3 | 3 | 10-Feb-15 | 12-Feb-15 | 10 |
| L1B-8204 | Mech Trim / Finish (HVAC & Plumbing) | 4 | 4 | 10-Feb-15 | 13-Feb-15 | 6 |

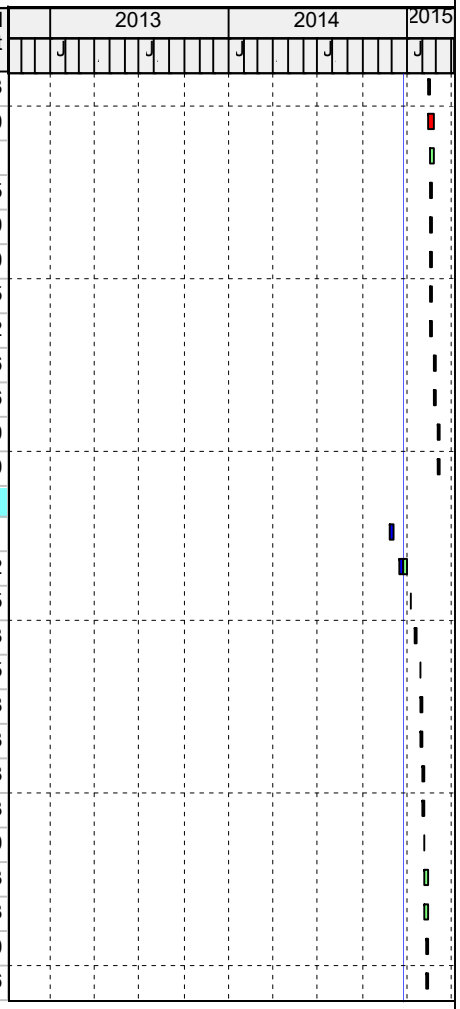



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-8214 | LL1 Zone 2 Compllete | 0 | 0 | | 10-Feb-15 | 18 |
| LL1-8201 | Final Coat Finish Paint | 4 | 4 | 11-Feb-15 | 16-Feb-15 | 10 |
| L1B-8201 | Final Coat Finish Paint | 5 | 5 | 16-Feb-15 | 20-Feb-15 | 6 |
| L1L-8204 | Mech Trim / Finish (HVAC & Plumbing) | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 5 |
| LL1-Z3-8214 | LL1, Zone 3 Complete | 0 | 0 | | 17-Feb-15 | 13 |
| L1K-8214 | L1, Zone 1 Complete | 0 | 0 | | 17-Feb-15 | 13 |
| LL1-8214 | LL1, Zone 1 Complete | 0 | 0 | | 20-Feb-15 | 10 |
| L1L-8201 | Final Coat Finish Paint | 3 | 3 | 26-Feb-15 | 02-Mar-15 | 0 |
| L1B-8214 | L1, Zone 2 Complete | 0 | 0 | | 26-Feb-15 | 6 |
| L1L-8214 | L1, Zone 4 Complete | 0 | 0 | | 06-Mar-15 | 0 |
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8100 | L2 - Insulation - North Half | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L02-8102 | L2 - GWB Hang / Tape / Finish - North Half | 7 | 0 | 23-Oct-14 A | 17-Dec-14 A | |
| L02-8104 | L2 - Int Painting - North Half | 3 | 3 | 22-Dec-14 | 24-Dec-14 | 20 |
| L02-8106 | L2 - Wallcoverings | 4 | 4 | 29-Dec-14 | 02-Jan-15 | 15 |
| L02-8124 | L2 - Flooring | 5 | 5 | 05-Jan-15 | 09-Jan-15 | 15 |
| L02-8108 | L2 - Elec Trim / Finish | 5 | 5 | 06-Jan-15 | 12-Jan-15 | 21 |
| L02-8110 | L2 - HVAC Trim / Finish | 5 | 5 | 06-Jan-15 | 12-Jan-15 | 21 |
| L02-8112 | L2 - Fire Sprinkler Trim / Finish | 5 | 5 | 06-Jan-15 | 12-Jan-15 | 21 |
| L02-8118 | L2 - Elec Specialties Trim / Finish | 5 | 5 | 06-Jan-15 | 12-Jan-15 | 21 |
| L02-8116 | L2 - Finish Carpentry / Millwork | 4 | 4 | 09-Jan-15 | 14-Jan-15 | 15 |
| L02-8120 | L2 - Ceramic Tile / Counter Tops | 5 | 5 | 09-Jan-15 | 15-Jan-15 | 15 |
| L02-8128 | L2 - Bath Specialties | 4 | 4 | 09-Jan-15 | 14-Jan-15 | 21 |
| L02-8122 | L2 - Plumbing Trim / Finish | 5 | 5 | 13-Jan-15 | 19-Jan-15 | 23 |
| L02-8126 | L2 - Doors & Hardware | 5 | 5 | 15-Jan-15 | 21-Jan-15 | 16 |
| L02-8136 | L2 - Lockers / Benches @ Locker Rooms | 5 | 5 | 16-Jan-15 | 22-Jan-15 | 15 |

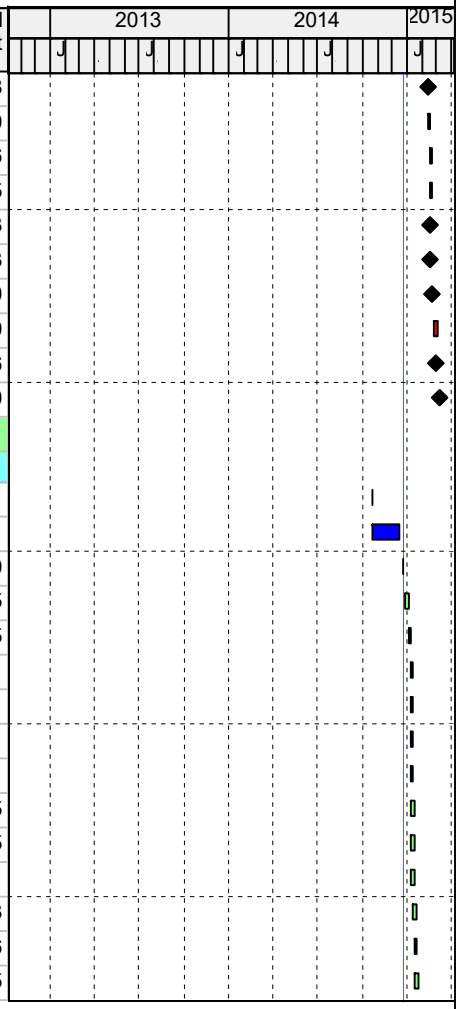



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8132 | L2 - Punch | 5 | 5 | 30-Jan-15 | 05-Feb-15 | 15 |
| L02-8134 | L2 - Clean | 5 | 5 | 30-Jan-15 | 05-Feb-15 | 15 |
| **Corridors** | | | | | | |
| L02-8200 | L2 - Final Paint @ Common / Public Areas | 5 | 5 | 23-Jan-15 | 29-Jan-15 | 15 |
| L02-8114 | L2 - Signage | 3 | 3 | 30-Jan-15 | 03-Feb-15 | 23 |
| L02-8210 | L2 - Owner Walk / Create Punchlist | 1 | 1 | 06-Feb-15 | 06-Feb-15 | 15 |
| L02-8212 | L2 - Resolve Final Punchlist | 5 | 5 | 09-Feb-15 | 13-Feb-15 | 15 |
| L02-8214 | Floor Complete | 0 | 0 | | 13-Feb-15 | 15 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L03-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L04-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L05-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L06-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L07-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L08-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L09-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L10-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L11-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L12-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L14-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L15-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L16-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L17-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L03-8102S | Stock GWB | 2 | 0 | 27-Jun-14 A | 08-Jul-14 A | |
| L04-8102 | Hang GWB & Inspection | 4 | 0 | 07-Jul-14 A | 16-Jul-14 A | |

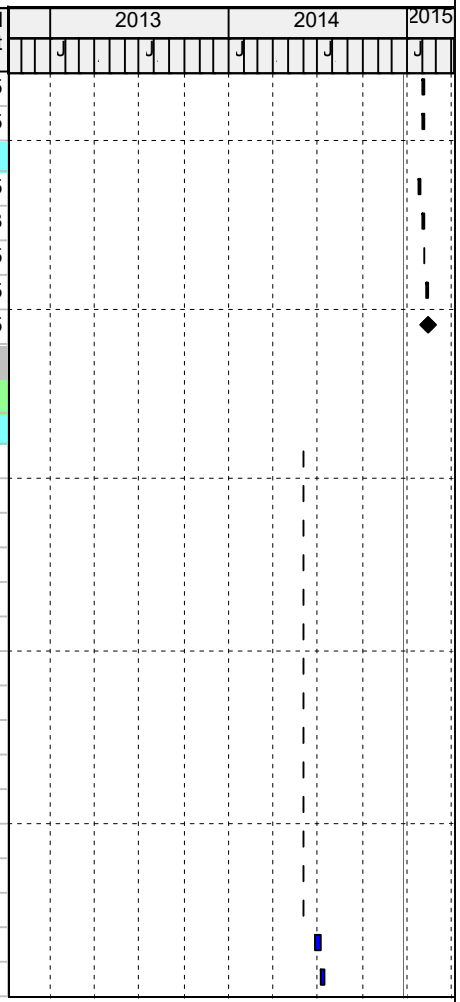



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8102S | Stock GWB | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-8102 | Hang GWB & Inspection | 5 | 0 | 09-Jul-14 A | 22-Jul-14 A | |
| L05-8102S | Stock GWB | 2 | 0 | 10-Jul-14 A | 14-Jul-14 A | |
| L05-8102 | Hang GWB & Inspection | 4 | 0 | 17-Jul-14 A | 23-Jul-14 A | |
| L06-8102S | Stock GWB | 2 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L04-8104 | Paint (Prime) | 2 | 0 | 28-Jul-14 A | 05-Aug-14 A | |
| L03-8104 | Paint (Prime) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L03-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L07-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L08-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L06-8102 | Hang GWB & Inspection | 5 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L07-8102 | Hang GWB & Inspection | 6 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L04-8105 | Paint (First Coat & Ceilings) | 5 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L05-8104 | Paint (Prime) | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| L09-8102S | Stock GWB | 2 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 07-Aug-14 A | 11-Aug-14 A | |
| L09-8102 | Hang GWB & Inspection | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| L08-8102 | Hang GWB & Inspection | 6 | 0 | 11-Aug-14 A | 15-Aug-14 A | |
| L06-8104 | Paint (Prime) | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L10-8102S | Stock GWB | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-8102 | Hang GWB & Inspection | 4 | 0 | 13-Aug-14 A | 18-Aug-14 A | |
| L06-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 14-Aug-14 A | 18-Aug-14 A | |
| L11-8102S | Stock GWB | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L07-8104 | Paint (Prime) | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L11-8102 | Hang GWB & Inspection | 4 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| L07-8105 | Paint (First Coat & Ceilings) | 4 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L09-8104 | Paint (Prime) | 2 | 0 | 20-Aug-14 A | 28-Aug-14 A | |

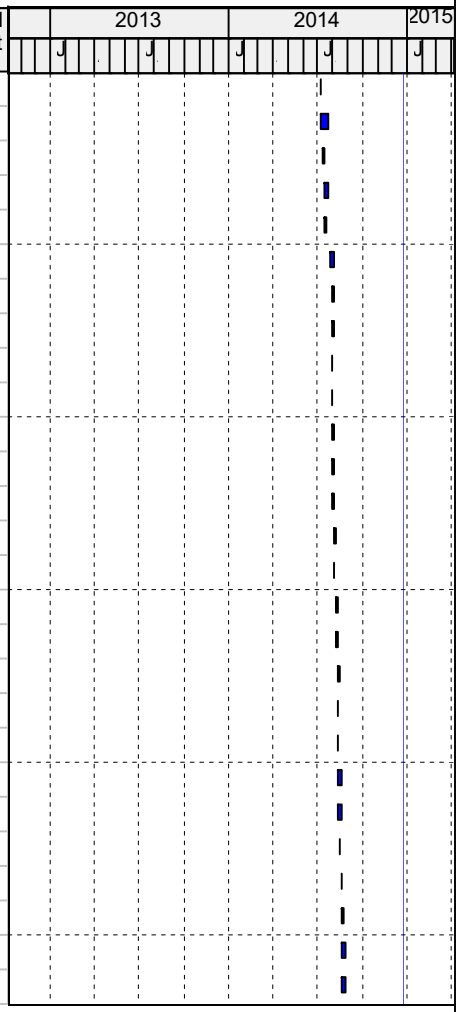



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8104 | Paint (Prime) | 2 | 0 | 22-Aug-14 A | 25-Aug-14 A | |
| L12-8102 | Hang GWB & Inspection | 4 | 0 | 22-Aug-14 A | 30-Aug-14 A | |
| L12-8102S | Stock GWB | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8108 | Elec Trim / Finish | 4 | 0 | 25-Aug-14 A | 04-Sep-14 A | |
| L08-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L03-8118 | Fire Alarm Trim / Finish | 3 | 0 | 27-Aug-14 A | 29-Sep-14 A | |
| L14-8102S | Stock GWB | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L09-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 29-Aug-14 A | 09-Sep-14 A | |
| L14-8102 | Hang GWB & Inspection | 5 | 0 | 29-Aug-14 A | 05-Sep-14 A | |
| L03-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 02-Sep-14 A | 05-Sep-14 A | |
| L04-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 04-Sep-14 A | 09-Sep-14 A | |
| L10-8104 | Paint (Prime) | 2 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| L15-8102S | Stock GWB | 1 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L15-8102 | Hang GWB & Inspection | 5 | 0 | 06-Sep-14 A | 12-Sep-14 A | |
| L03-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8108 | Elec Trim / Finish | 4 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L04-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 11-Sep-14 A | |
| L05-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 08-Sep-14 A | 12-Sep-14 A | |
| L10-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 08-Sep-14 A | 12-Sep-14 A | |
| L11-8104 | Paint (Prime) | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L04-8116 | Install Base at Guestrooms | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L11-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 10-Sep-14 A | 22-Sep-14 A | |
| L03-8116 | Install Base at Guestrooms | 5 | 0 | 12-Sep-14 A | 16-Sep-14 A | |
| L12-8104 | Paint (Prime) | 2 | 0 | 12-Sep-14 A | 17-Sep-14 A | |
| L05-8116 | Install Base at Guestrooms | 5 | 0 | 16-Sep-14 A | 24-Sep-14 A | |
| L06-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 16-Sep-14 A | 22-Sep-14 A | |

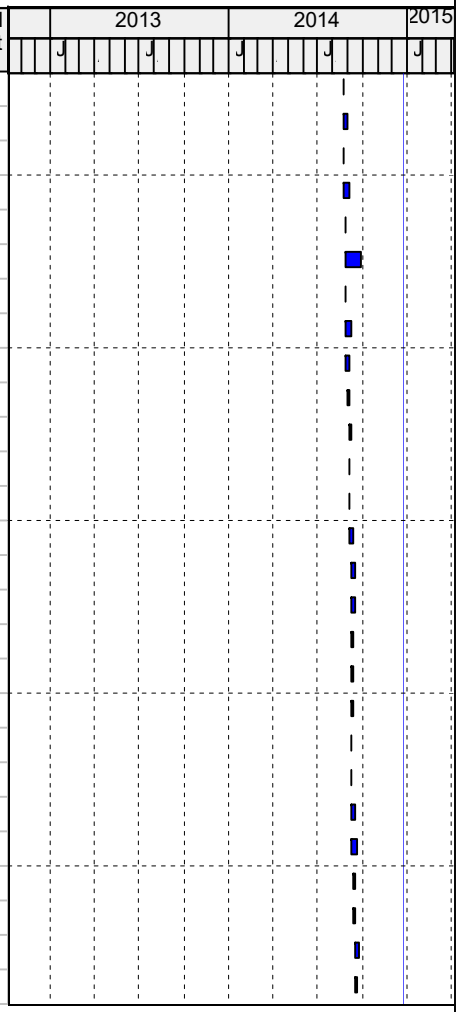



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8108 | Elec Trim / Finish | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L07-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 17-Sep-14 A | 23-Sep-14 A | |
| L12-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 17-Sep-14 A | 06-Oct-14 A | |
| L06-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L07-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L14-8104 | Paint (Prime) | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L06-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L06-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L08-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L14-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 24-Sep-14 A | 06-Oct-14 A | |
| L15-8104 | Paint (Prime) | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L03-8110 | HVAC Grilles & Registers | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L03-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8118 | Fire Alarm Trim / Finish | 3 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L10-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L08-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 30-Sep-14 A | 06-Oct-14 A | |
| L03-8126 | Install Doors | 3 | 0 | 01-Oct-14 A | 07-Oct-14 A | |
| L03-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 01-Oct-14 A | 28-Oct-14 A | |
| L04-8126 | Install Doors | 3 | 0 | 02-Oct-14 A | 09-Oct-14 A | |
| L08-8116 | Install Base at Guestrooms | 5 | 0 | 02-Oct-14 A | 08-Oct-14 A | |
| L04-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8118 | Fire Alarm Trim / Finish | 3 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8108 | Elec Trim / Finish | 4 | 0 | 06-Oct-14 A | 08-Oct-14 A | |

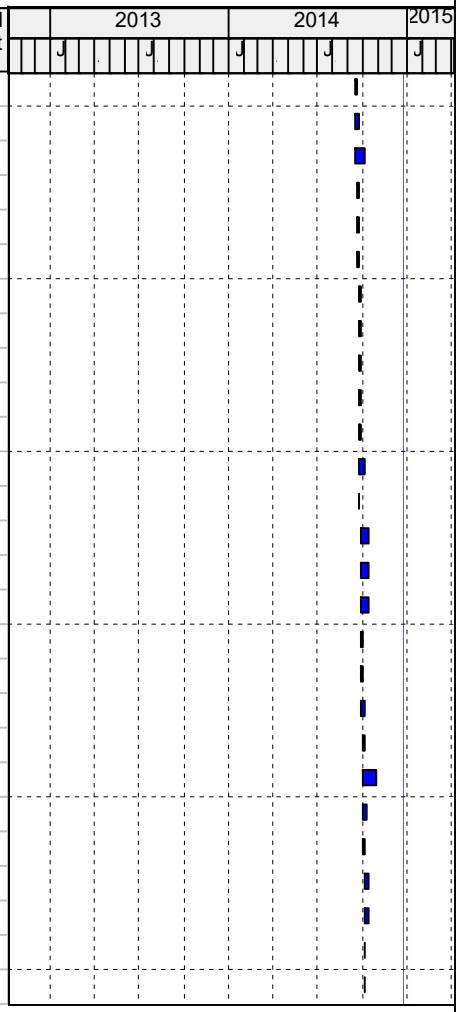


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8105 | Paint - First Coast & Ceilings | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8126 | Install Doors | 3 | 0 | 08-Oct-14 A | 10-Oct-14 A | |
| L09-8116 | Install Base and Door Thresholds | 5 | 0 | 08-Oct-14 A | 15-Oct-14 A | |
| L09-8124 | Install Flooring | 5 | 0 | 08-Oct-14 A | 14-Oct-14 A | |
| L16-8102S | Stock GWB | 1 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L09-8112 | Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 10-Oct-14 A | |
| L16-8102 | Hang GWB & Inspection | 4 | 0 | 10-Oct-14 A | 17-Oct-14 A | |
| L06-8118 | Fire Alarm Trim / Finish | 3 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L09-8108 | Lighting and Electrical Trim | 3 | 0 | 13-Oct-14 A | 15-Oct-14 A | |
| L10-8124 | Install Flooring | 5 | 0 | 13-Oct-14 A | 16-Oct-14 A | |
| L11-8112 | Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L03-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 14-Oct-14 A | 04-Nov-14 A | |
| L06-8110 | HVAC Grilles & Registers | 2 | 0 | 14-Oct-14 A | 21-Oct-14 A | |
| L06-8126 | Install Doors | 2 | 0 | 14-Oct-14 A | 20-Oct-14 A | |
| L07-8118 | Fire Alarm Trim / Finish | 3 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L12-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L14-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L08-8118 | Fire Alarm Trim / Finish | 3 | 0 | 15-Oct-14 A | 16-Oct-14 A | |
| L10-8116 | Install Base and Door Thresholds | 5 | 0 | 15-Oct-14 A | 23-Oct-14 A | |
| L15-8112 | Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 16-Oct-14 A | |
| L04-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 16-Oct-14 A | 11-Nov-14 A | |
| L11-8124 | Install Flooring | 5 | 0 | 16-Oct-14 A | 22-Oct-14 A | |
| L17-8102S | Stock GWB | 1 | 0 | 17-Oct-14 A | 17-Oct-14 A | |
| L07-8126 | Install Doors | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |
| L09-8118 | Fire Alarm Trim | 2 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| L05-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 21-Oct-14 A | 14-Nov-14 A | |
| L08-8126 | Install Doors | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |

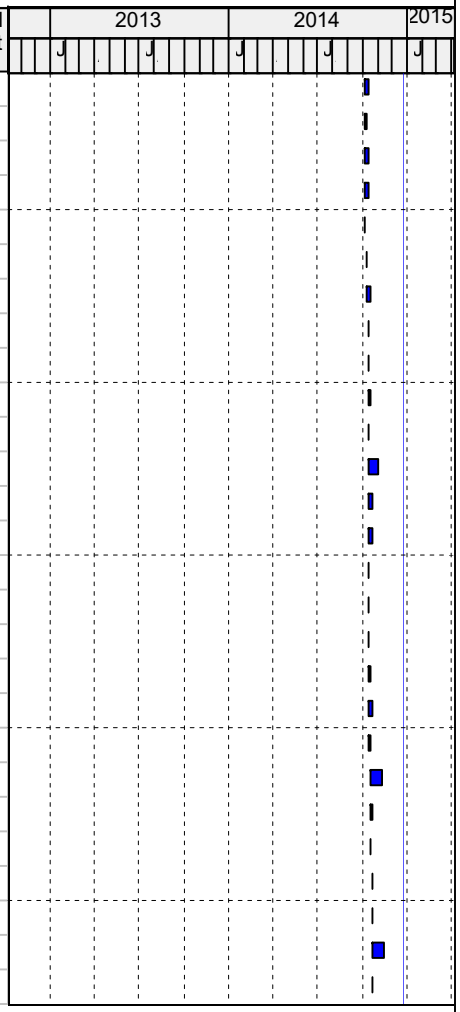



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8118 | Fire Alarm Trim | 2 | 0 | 21-Oct-14 A | 21-Oct-14 A | |
| L09-8126 | Install Doors | 2 | 0 | 22-Oct-14 A | 23-Oct-14 A | |
| L11-8118 | Fire Alarm Trim | 2 | 0 | 22-Oct-14 A | 22-Oct-14 A | |
| L06-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 23-Oct-14 A | 19-Nov-14 A | |
| L10-8126 | Install Doors | 2 | 0 | 23-Oct-14 A | 27-Oct-14 A | |
| L12-8124 | Install Flooring | 5 | 0 | 23-Oct-14 A | 29-Oct-14 A | |
| L12-8118 | Fire Alarm Trim | 2 | 0 | 23-Oct-14 A | 23-Oct-14 A | |
| L11-8116 | Install Base and Door Thresholds | 5 | 0 | 24-Oct-14 A | 26-Nov-14 A | |
| L07-8110 | HVAC Grilles & Registers | 2 | 0 | 27-Oct-14 A | 28-Oct-14 A | |
| L10-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |
| L11-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |
| L17-8102 | Hang GWB & Inspection | 4 | 0 | 27-Oct-14 A | 03-Nov-14 A | |
| L07-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 28-Oct-14 A | 26-Nov-14 A | |
| L08-8120 | Bathrooms - Install Countertops | 3 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L11-8126 | Install Doors | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L12-8108 | Lighting and Electrical Trim | 3 | 0 | 28-Oct-14 A | 30-Oct-14 A | |
| L12-8116 | Install Base and Door Thresholds | 5 | 0 | 28-Oct-14 A | 03-Dec-14 A | |
| L14-8118 | Fire Alarm Trim | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L05-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Oct-14 A | 31-Oct-14 A | |
| L06-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Oct-14 A | 31-Oct-14 A | |
| L12-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L14-8108 | Lighting and Electrical Trim | 3 | 0 | 29-Oct-14 A | 03-Nov-14 A | |
| L14-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8118 | Fire Alarm Trim | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L04-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 30-Oct-14 A | 04-Nov-14 A | |
| L07-8120 | Bathrooms - Install Countertops | 3 | 0 | 03-Nov-14 A | 05-Nov-14 A | |

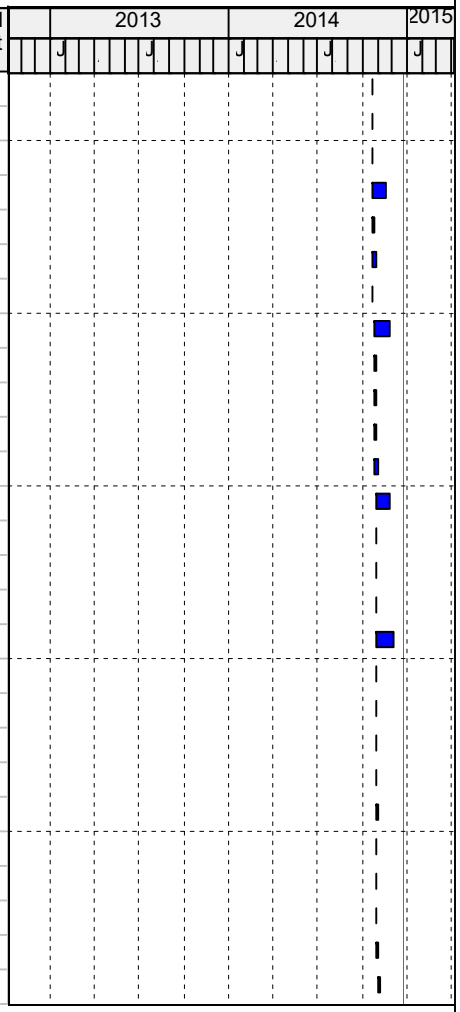


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8110 | HVAC Grilles & Registers | 2 | 0 | 03-Nov-14 A | 04-Nov-14 A | |
| L09-8120 | Bathrooms - Install Countertops | 3 | 0 | 03-Nov-14 A | 05-Nov-14 A | |
| L10-8120 | Bathrooms - Install Countertops | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| L15-8108 | Lighting and Electrical Trim | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| L11-8120 | Bathrooms - Install Countertops | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| L16-8104 | Paint - Prime | 2 | 0 | 05-Nov-14 A | 06-Nov-14 A | |
| L05-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 07-Nov-14 A | 12-Nov-14 A | |
| L16-8105 | Paint - First Coat & Ceilings | 3 | 0 | 07-Nov-14 A | 11-Nov-14 A | |
| L12-8120 | Bathrooms - Install Countertops | 3 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L14-8124 | Install Flooring | 5 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L06-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 13-Nov-14 A | 17-Nov-14 A | |
| L15-8124 | Install Flooring | 5 | 0 | 17-Nov-14 A | 25-Nov-14 A | |
| L17-8104 | Paint - Prime | 2 | 0 | 17-Nov-14 A | 18-Nov-14 A | |
| L14-8116 | Install Base and Door Thresholds | 5 | 0 | 18-Nov-14 A | 08-Dec-14 A | |
| L16-8126 | Install Doors | 2 | 0 | 18-Nov-14 A | 19-Nov-14 A | |
| L07-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 19-Nov-14 A | 25-Nov-14 A | |
| L15-8116 | Install Base and Door Thresholds | 5 | 0 | 20-Nov-14 A | 08-Dec-14 A | |
| L03-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L04-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L05-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L08-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| L17-8105 | Paint - First Coat & Ceilings | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L16-8124 | Install Flooring | 5 | 0 | 25-Nov-14 A | 03-Dec-14 A | |
| L16-8112 | Fire Sprinkler Trim | 2 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| L16-8118 | Fire Alarm Trim | 2 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| L06-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L07-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |

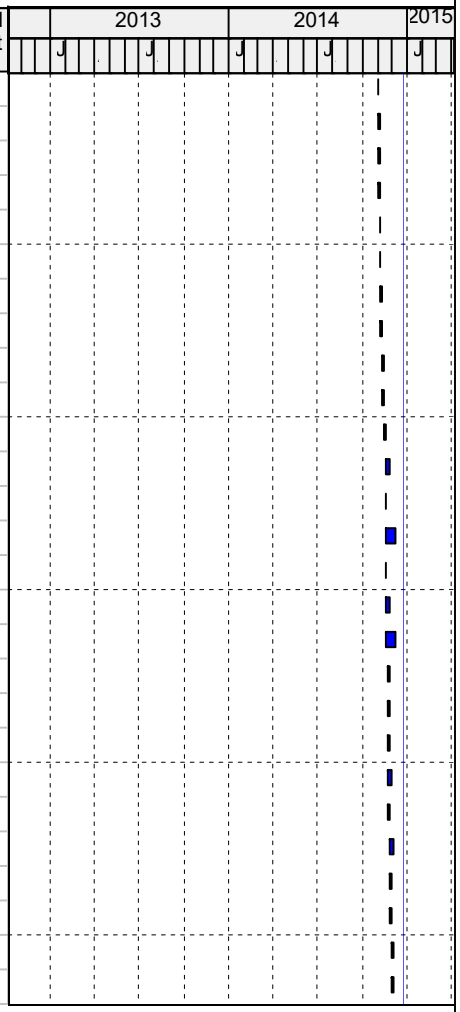



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 01-Dec-14 A | 08-Dec-14 A | |
| L08-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L09-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 01-Dec-14 A | 10-Dec-14 A | |
| L16-8108 | Lighting and Electrical Trim | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L17-8126 | Install Doors | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| L16-8116 | Install Base and Door Thresholds | 5 | 0 | 02-Dec-14 A | 15-Dec-14 A | |
| L17-8112 | Fire Sprinkler Trim | 2 | 0 | 02-Dec-14 A | 02-Dec-14 A | |
| L09-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 03-Dec-14 A | 08-Dec-14 A | |
| L09-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L10-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L11-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L17-8118 | Fire Alarm Trim | 2 | 0 | 03-Dec-14 A | 03-Dec-14 A | |
| L12-8107 | Paint Final Coat | 3 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L14-8120 | Bathrooms - Install Countertops | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L17-8108 | Lighting and Electrical Trim | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L10-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L15-8120 | Bathrooms - Install Countertops | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 10-Dec-14 A | 16-Dec-14 A | |
| L11-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 3 | 10-Dec-14 A | 24-Dec-14 | 34 |
| L04-8132 | Punchlist @ Guestrooms | 4 | 2 | 11-Dec-14 A | 23-Dec-14 | 32 |
| L04-8134 | Final Clean @ Guestrooms | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L05-8132 | Punchlist @ Guestrooms | 4 | 3 | 12-Dec-14 A | 24-Dec-14 | 31 |
| L05-8134 | Final Clean @ Guestrooms | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L11-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 12-Dec-14 A | 17-Dec-14 A | |
| L06-8134 | Final Clean @ Guestrooms | 5 | 0 | 13-Dec-14 A | 13-Dec-14 A | |
| L12-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 15-Dec-14 A | 18-Dec-14 A | |
| L17-8124 | Install Flooring | 5 | 0 | 15-Dec-14 A | 18-Dec-14 A | |

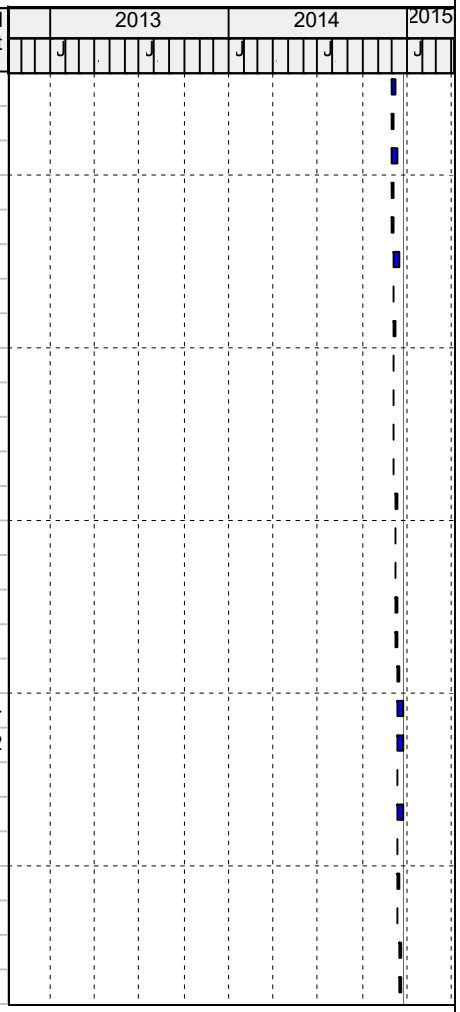


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8116 | Install Base and Door Thresholds | 5 | 3 | 18-Dec-14 A | 30-Dec-14 | 16 |
| L04-8109 | Corridors - Acoustical Ceiling Tile | 1 | 1 | 22-Dec-14 | 22-Dec-14 | 46 |
| L05-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 32 |
| L07-8134 | Final Clean @ Guestrooms | 1 | 1 | 22-Dec-14 | 22-Dec-14 | 32 |
| L08-8134 | Final Clean @ Guestrooms | 1 | 1 | 22-Dec-14 | 22-Dec-14 | 32 |
| L09-8110 | HVAC Grilles & Registers | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 20 |
| L10-8110 | HVAC Grilles & Registers | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 20 |
| L11-8110 | HVAC Grilles & Registers | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 22 |
| L12-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 22-Dec-14 | 29-Dec-14 | 34 |
| L12-8110 | HVAC Grilles & Registers | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 22 |
| L14-8110 | HVAC Grilles & Registers | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 21 |
| L14-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 22-Dec-14 | 29-Dec-14 | 31 |
| L15-8110 | HVAC Grilles & Registers | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 21 |
| L15-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 22-Dec-14 | 29-Dec-14 | 31 |
| L16-8110 | HVAC Grilles & Registers | 2 | 2 | 22-Dec-14 | 23-Dec-14 | 23 |
| L16-8120 | Bathrooms - Install Countertops | 3 | 3 | 22-Dec-14 | 24-Dec-14 | 20 |
| L06-8132 | Punchlist @ Guestrooms | 4 | 4 | 23-Dec-14 | 30-Dec-14 | 29 |
| L06-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 31 |
| L07-8132 | Punchlist @ Guestrooms | 4 | 4 | 23-Dec-14 | 30-Dec-14 | 29 |
| L07-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 66 |
| L08-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 31 |
| L09-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 23-Dec-14 | 24-Dec-14 | 31 |
| L03-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 36 |
| L08-8132 | Punchlist @ Guestrooms | 3 | 3 | 24-Dec-14 | 30-Dec-14 | 29 |
| L09-8132 | Punchlist @ Guestrooms | 3 | 3 | 24-Dec-14 | 30-Dec-14 | 29 |
| L09-8134 | Final Clean @ Guestrooms | 1 | 1 | 24-Dec-14 | 24-Dec-14 | 31 |
| L10-8132 | Punchlist @ Guestrooms | 3 | 3 | 24-Dec-14 | 30-Dec-14 | 29 |

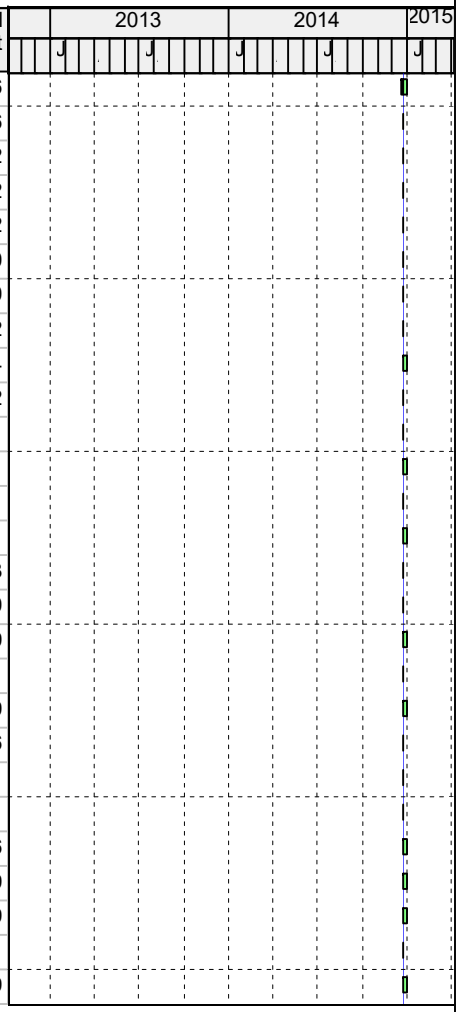



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8134 | Final Clean @ Guestrooms | 1 | 1 | 24-Dec-14 | 24-Dec-14 | 31 |
| L10-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 30 |
| L11-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 37 |
| L12-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 38 |
| L14-8107 | Paint Final Coat | 3 | 3 | 24-Dec-14 | 30-Dec-14 | 21 |
| L14-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 39 |
| L15-8107 | Paint Final Coat | 3 | 3 | 24-Dec-14 | 30-Dec-14 | 21 |
| L15-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 39 |
| L16-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 24-Dec-14 | 29-Dec-14 | 41 |
| L16-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 29-Dec-14 | 02-Jan-15 | 30 |
| L14-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 30-Dec-14 | 05-Jan-15 | 31 |
| L15-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 30-Dec-14 | 05-Jan-15 | 31 |
| L17-8120 | Bathrooms - Install Countertops | 3 | 3 | 30-Dec-14 | 02-Jan-15 | 16 |
| L16-8107 | Paint Final Coat | 3 | 3 | 31-Dec-14 | 05-Jan-15 | 20 |
| L17-8110 | HVAC Grilles & Registers | 2 | 2 | 31-Dec-14 | 02-Jan-15 | 18 |
| L16-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 05-Jan-15 | 08-Jan-15 | 30 |
| L17-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 4 | 05-Jan-15 | 08-Jan-15 | 25 |
| L17-8107 | Paint - Final Coat | 3 | 3 | 07-Jan-15 | 09-Jan-15 | 16 |
| L17-8109 | Corridors - Acoustical Ceiling Tile | 2 | 2 | 07-Jan-15 | 08-Jan-15 | 33 |
| L17-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 4 | 09-Jan-15 | 14-Jan-15 | 25 |
| L11-8132 | Punchlist @ Guestrooms | 4 | 4 | 29-Jan-15* | 03-Feb-15 | 17 |
| L12-8132 | Punchlist @ Guestrooms | 4 | 4 | 29-Jan-15 | 03-Feb-15 | 17 |
| L14-8132 | Punchlist @ Guestrooms | 4 | 4 | 02-Feb-15 | 05-Feb-15 | 16 |
| L15-8132 | Punchlist @ Guestrooms | 4 | 4 | 02-Feb-15 | 05-Feb-15 | 16 |
| L03-8132 | Punchlist @ Guestrooms | 4 | 4 | 03-Feb-15 | 06-Feb-15 | 14 |
| L03-8134 | Final Clean @ Guestrooms | 1 | 1 | 03-Feb-15* | 03-Feb-15 | 12 |
| L11-8134 | Final Clean @ Guestrooms | 1 | 1 | 04-Feb-15 | 04-Feb-15 | 12 |

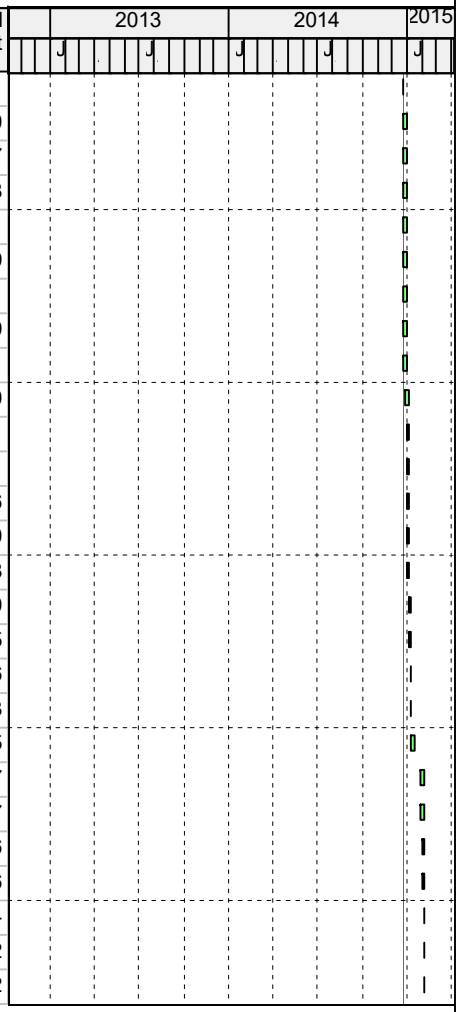


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8132 | Punchlist @ Guestrooms | 3 | 3 | 04-Feb-15 | 06-Feb-15 | 19 |
| L17-8132 | Punchlist @ Guestrooms | 3 | 3 | 04-Feb-15 | 06-Feb-15 | 15 |
| L12-8134 | Final Clean @ Guestrooms | 1 | 1 | 05-Feb-15 | 05-Feb-15 | 12 |
| L14-8134 | Final Clean @ Guestrooms | 1 | 1 | 06-Feb-15 | 06-Feb-15 | 12 |
| L15-8134 | Final Clean @ Guestrooms | 1 | 1 | 09-Feb-15 | 09-Feb-15 | 12 |
| L16-8134 | Final Clean @ Guestrooms | 1 | 1 | 10-Feb-15 | 10-Feb-15 | 14 |
| L17-8134 | Final Clean @ Guestrooms | 1 | 1 | 11-Feb-15 | 11-Feb-15 | 12 |
| **Pool Area** | | | | | | |
| L03-8216 | L3 Pool - Install tile, coping and depth markers | 5 | 5 | 27-Jan-15 | 02-Feb-15 | 32 |
| **Corridors / Common / Public Areas** | | | | | | |
| L03-8200 | Vinyl Wall Coverings | 3 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L04-8200 | Vinyl Wall Coverings | 5 | 0 | 06-Aug-14 A | 12-Aug-14 A | |
| L05-8200 | Vinyl Wall Coverings | 5 | 0 | 12-Aug-14 A | 22-Sep-14 A | |
| L03-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L06-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L08-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 11-Sep-14 A | 19-Sep-14 A | |
| L04-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| L05-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L06-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L07-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L09-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| L10-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 08-Oct-14 A | |
| L11-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 10-Oct-14 A | |
| L08-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L12-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| L09-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |

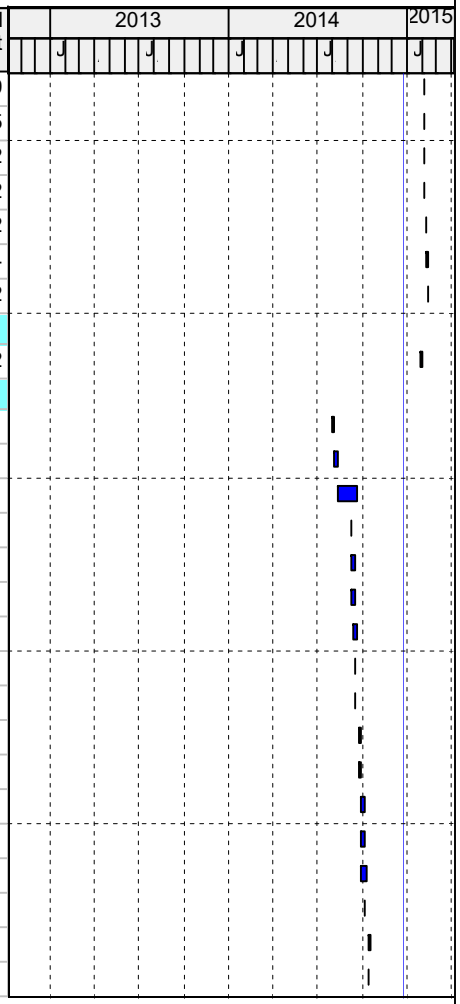



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 16-Oct-14 A | 27-Oct-14 A | |
| L10-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |
| L11-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L15-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 22-Oct-14 A | 29-Oct-14 A | |
| L12-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 03-Nov-14 A | 04-Nov-14 A | |
| L14-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L15-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 05-Nov-14 A | 06-Nov-14 A | |
| L16-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 14-Nov-14 A | 20-Nov-14 A | |
| L16-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L17-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L17-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 2 | 15-Dec-14 A | 23-Dec-14 | 16 |
| L04-8206 | Corridors - Flooring & Base | 3 | 3 | 12-Jan-15* | 14-Jan-15 | 3 |
| L05-8206 | Corridors - Flooring & Base | 2 | 2 | 15-Jan-15 | 16-Jan-15 | 3 |
| L06-8206 | Corridors - Flooring & Base | 2 | 2 | 15-Jan-15 | 16-Jan-15 | 3 |
| L07-8206 | Corridors - Flooring & Base | 2 | 2 | 19-Jan-15 | 20-Jan-15 | 3 |
| L08-8206 | Corridors - Flooring & Base | 2 | 2 | 19-Jan-15 | 20-Jan-15 | 3 |
| L09-8206 | Corridors - Flooring & Base | 2 | 2 | 21-Jan-15 | 22-Jan-15 | 3 |
| L10-8206 | Corridors - Flooring & Base | 2 | 2 | 21-Jan-15 | 22-Jan-15 | 3 |
| L11-8206 | Corridors - Flooring & Base | 2 | 2 | 23-Jan-15 | 26-Jan-15 | 3 |
| L12-8206 | Corridors - Flooring & Base | 2 | 2 | 23-Jan-15 | 26-Jan-15 | 3 |
| L04-8208 | Final Clean (Entire Floor) | 2 | 2 | 27-Jan-15 | 28-Jan-15 | 24 |
| L14-8206 | Corridors - Flooring & Base | 2 | 2 | 27-Jan-15 | 28-Jan-15 | 3 |
| L15-8206 | Corridors - Flooring & Base | 2 | 2 | 27-Jan-15 | 28-Jan-15 | 3 |
| L03-8206 | Corridors - Flooring & Base | 2 | 2 | 28-Jan-15 | 29-Jan-15 | 4 |
| L04-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 29-Jan-15 | 29-Jan-15 | 24 |
| L05-8208 | Final Clean (Entire Floor) | 2 | 2 | 29-Jan-15 | 30-Jan-15 | 22 |
| L16-8206 | Corridors - Flooring & Base | 2 | 2 | 29-Jan-15 | 30-Jan-15 | 3 |

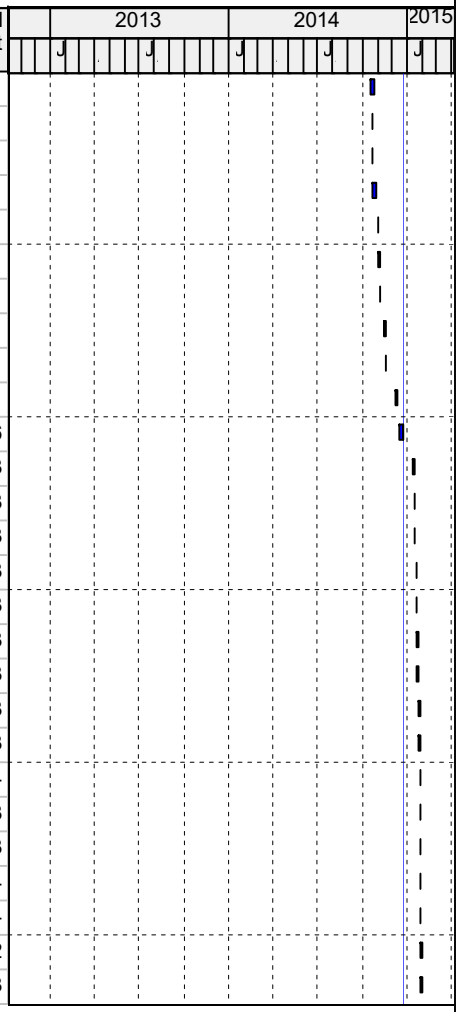



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8206 | Corridors - Flooring & Base | 2 | 2 | 29-Jan-15 | 30-Jan-15 | 3 |
| L04-8212 | Resolve Final Punchlist | 2 | 2 | 30-Jan-15 | 02-Feb-15 | 24 |
| L06-8208 | Final Clean (Entire Floor) | 2 | 2 | 30-Jan-15 | 02-Feb-15 | 21 |
| L05-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 22 |
| L07-8208 | Final Clean (Entire Floor) | 2 | 2 | 02-Feb-15 | 03-Feb-15 | 20 |
| L04-8214 | Floor Complete | 0 | 0 | | 02-Feb-15 | 24 |
| L05-8212 | Resolve Final Punchlist | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 22 |
| L06-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 21 |
| L08-8208 | Final Clean (Entire Floor) | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 19 |
| L06-8212 | Resolve Final Punchlist | 2 | 2 | 04-Feb-15 | 05-Feb-15 | 21 |
| L07-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 04-Feb-15 | 04-Feb-15 | 20 |
| L09-8208 | Final Clean (Entire Floor) | 2 | 2 | 04-Feb-15 | 05-Feb-15 | 18 |
| L05-8214 | Floor Complete | 0 | 0 | | 04-Feb-15 | 22 |
| L07-8212 | Resolve Final Punchlist | 2 | 2 | 05-Feb-15 | 06-Feb-15 | 20 |
| L08-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 05-Feb-15 | 05-Feb-15 | 19 |
| L10-8208 | Final Clean (Entire Floor) | 2 | 2 | 05-Feb-15 | 06-Feb-15 | 17 |
| L11-8208 | Final Clean (Entire Floor) | 2 | 2 | 05-Feb-15 | 06-Feb-15 | 17 |
| L06-8214 | Floor Complete | 0 | 0 | | 05-Feb-15 | 21 |
| L08-8212 | Resolve Final Punchlist | 2 | 2 | 06-Feb-15 | 09-Feb-15 | 19 |
| L09-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 06-Feb-15 | 06-Feb-15 | 18 |
| L12-8208 | Final Clean (Entire Floor) | 2 | 2 | 06-Feb-15 | 09-Feb-15 | 16 |
| L07-8214 | Floor Complete | 0 | 0 | | 06-Feb-15 | 20 |
| L09-8212 | Resolve Final Punchlist | 2 | 2 | 09-Feb-15 | 10-Feb-15 | 18 |
| L10-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 09-Feb-15 | 09-Feb-15 | 17 |
| L11-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 09-Feb-15 | 09-Feb-15 | 17 |
| L14-8208 | Final Clean (Entire Floor) | 2 | 2 | 09-Feb-15 | 10-Feb-15 | 15 |
| L08-8214 | Floor Complete | 0 | 0 | | 09-Feb-15 | 19 |

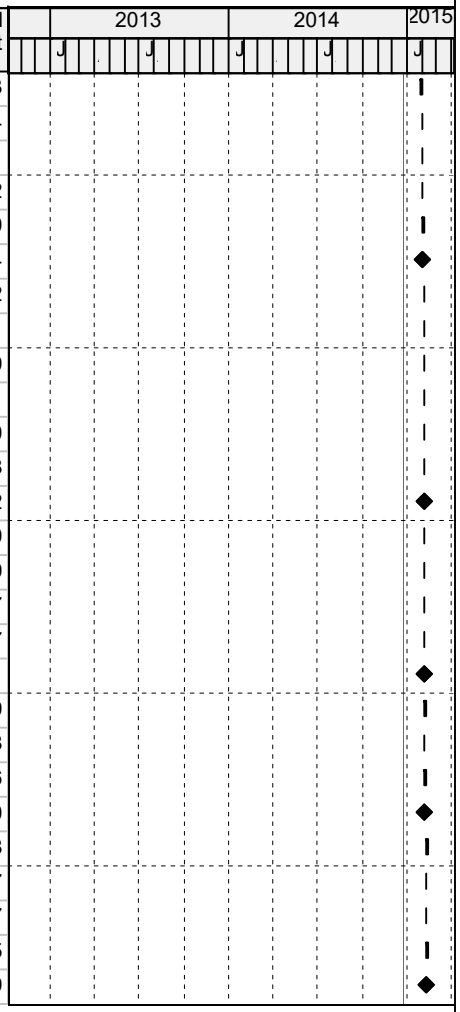



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8212 | Resolve Final Punchlist | 2 | 2 | 10-Feb-15 | 11-Feb-15 | 17 |
| L11-8212 | Resolve Final Punchlist | 2 | 2 | 10-Feb-15 | 11-Feb-15 | 17 |
| L12-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 10-Feb-15 | 10-Feb-15 | 16 |
| L15-8208 | Final Clean (Entire Floor) | 2 | 2 | 10-Feb-15 | 11-Feb-15 | 14 |
| L09-8214 | Floor Complete | 0 | 0 | | 10-Feb-15 | 18 |
| L03-8208 | Final Clean (Entire Floor) | 2 | 2 | 11-Feb-15 | 12-Feb-15 | 12 |
| L03-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 11-Feb-15 | 11-Feb-15 | 12 |
| L12-8212 | Resolve Final Punchlist | 2 | 2 | 11-Feb-15 | 12-Feb-15 | 16 |
| L14-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 11-Feb-15 | 11-Feb-15 | 15 |
| L16-8208 | Final Clean (Entire Floor) | 2 | 2 | 11-Feb-15 | 12-Feb-15 | 13 |
| L10-8214 | Floor Complete | 0 | 0 | | 11-Feb-15 | 17 |
| L11-8214 | Floor Complete | 0 | 0 | | 11-Feb-15 | 17 |
| L03-8212 | Resolve Final Punchlist | 5 | 5 | 12-Feb-15 | 18-Feb-15 | 12 |
| L14-8212 | Resolve Final Punchlist | 2 | 2 | 12-Feb-15 | 13-Feb-15 | 15 |
| L15-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 12-Feb-15 | 12-Feb-15 | 14 |
| L17-8208 | Final Clean (Entire Floor) | 2 | 2 | 12-Feb-15 | 13-Feb-15 | 12 |
| L12-8214 | Floor Complete | 0 | 0 | | 12-Feb-15 | 16 |
| L15-8212 | Resolve Final Punchlist | 2 | 2 | 13-Feb-15 | 16-Feb-15 | 14 |
| L16-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 13-Feb-15 | 13-Feb-15 | 13 |
| L14-8214 | Floor Complete | 0 | 0 | | 13-Feb-15 | 15 |
| L16-8212 | Resolve Final Punchlist | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 13 |
| L17-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 12 |
| L15-8214 | Floor Complete | 0 | 0 | | 16-Feb-15 | 14 |
| L17-8212 | Resolve Final Punchlist | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 12 |
| L16-8214 | Floor Complete | 0 | 0 | | 17-Feb-15 | 13 |
| L03-8214 | Floor Complete | 0 | 0 | | 18-Feb-15 | 12 |
| L17-8214 | Floor Complete | 0 | 0 | | 18-Feb-15 | 12 |

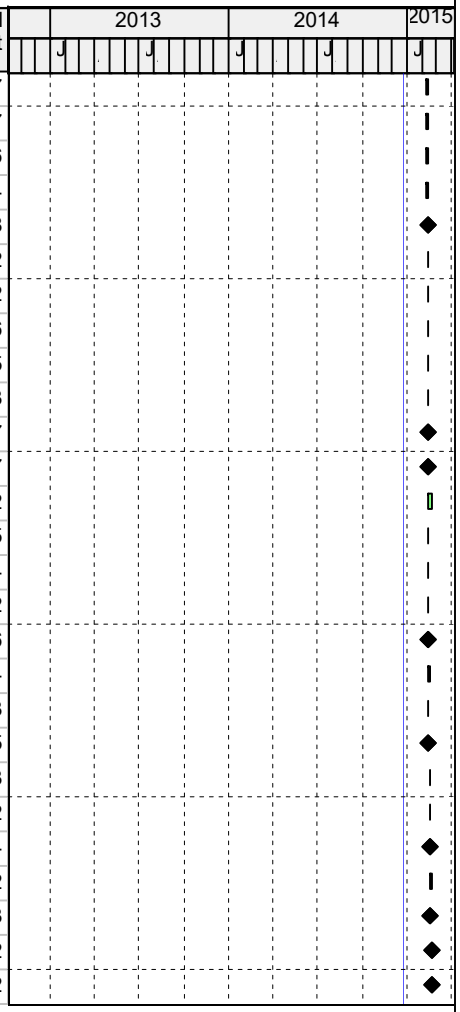



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Mech Penthouse** | | | | | | |
| PH-8100 | PH - Insulation & Vapor Barrier | 5 | 0 | 09-Oct-14 A | 13-Oct-14 A | |
| PH-8102 | PH - Complete GWB Hang / Tape / Finish | 6 | 0 | 14-Oct-14 A | 10-Nov-14 A | |
| PH-8122 | PH - Plumbing Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8110 | PH - HVAC Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8126 | PH - Doors & Hardware | 2 | 1 | 24-Nov-14 A | 22-Dec-14 | 58 |
| PH-8104 | PH - Int Painting [DELETED] | 4 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| PH-8108 | PH - Elec Trim / Finish | 5 | 2 | 01-Dec-14 A | 23-Dec-14 | 54 |
| PH-8114 | PH - Install Stairs to Roof [DELETED] | 1 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| PH-8118 | PH - Elec Specialties Trim / Finish | 5 | 2 | 01-Dec-14 A | 23-Dec-14 | 54 |
| PH-8124 | PH - Flooring | 5 | 5 | 22-Dec-14 | 30-Dec-14 | 54 |
| PH-8132 | PH - Contractor Pre-Punchlist | 1 | 1 | 31-Dec-14 | 31-Dec-14 | 56 |
| PH-8134 | PH - Final Trims and Touch-Up | 3 | 3 | 31-Dec-14 | 05-Jan-15 | 54 |
| PH-8208 | PH - Final Clean | 1 | 1 | 06-Jan-15 | 06-Jan-15 | 54 |
| PH-8212 | PH - Final Punchlist | 1 | 1 | 07-Jan-15 | 07-Jan-15 | 54 |
| PH-8214 | PH - Floor Complete | 0 | 0 | | 07-Jan-15 | 54 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| **Smoke Control** | | | | | | |
| CO-7104 | Smoke Control Pre-Testing (Podium) | 5 | 5 | 09-Mar-15 | 13-Mar-15 | 2 |
| CO-7106 | City of Bellevue Smoke Control Testing (Podium) | 5 | 5 | 16-Mar-15 | 20-Mar-15 | 2 |
| CO-7108 | Final Marriott Smoke Control Testing | 5 | 5 | 25-Mar-15 | 31-Mar-15 | 0 |
| **Fire Sprinklers** | | | | | | |
| CO-7110 | Fire Sprinkler Pre-Testing (Podium) | 5 | 5 | 02-Mar-15 | 06-Mar-15 | 2 |
| CO-7112 | City of Bellevue Fire Sprinkler Inspection / Approval (F | 5 | 5 | 16-Mar-15 | 20-Mar-15 | 2 |
| CO-7114 | Marriott Fire Sprinkler Testing | 5 | 5 | 25-Mar-15 | 31-Mar-15 | 0 |
| **Fire Alarm** | | | | | | |

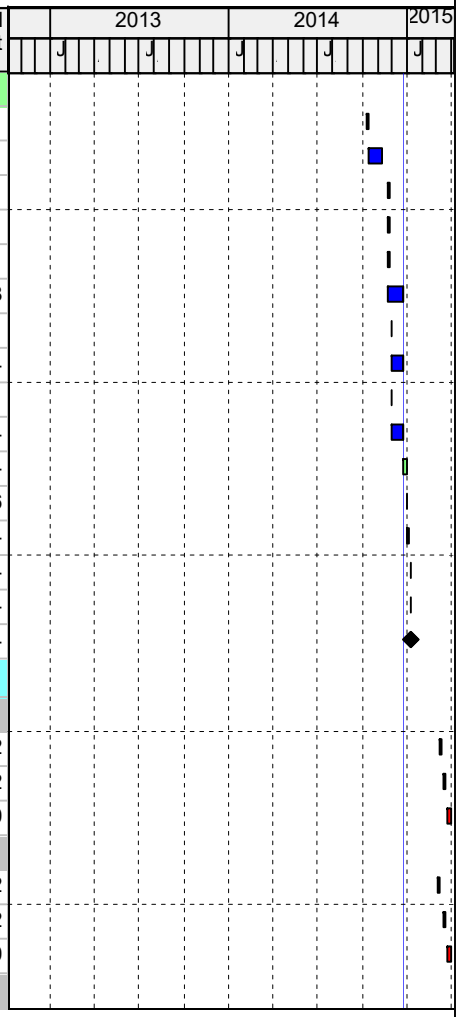



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7116 | Fire Alarm Pre-Testing (Podium) | 5 | 5 | 02-Mar-15 | 06-Mar-15 | 2 |
| CO-7118 | City of Bellevue Fire Alarm Inspection / Approval (Pod | 5 | 5 | 16-Mar-15 | 20-Mar-15 | 2 |
| CO-7120 | Marriott Fire Alarm Testing | 5 | 5 | 25-Mar-15 | 31-Mar-15 | 0 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| CO-7100 | Cx - Start-Up - Garage Exhaust Fan and VFD's | 4 | 4 | 22-Dec-14* | 29-Dec-14 | 29 |
| CO-7102 | Cx - DDC Point-To-Point - Garage Exhaust Fans | 5 | 5 | 30-Dec-14 | 06-Jan-15 | 55 |

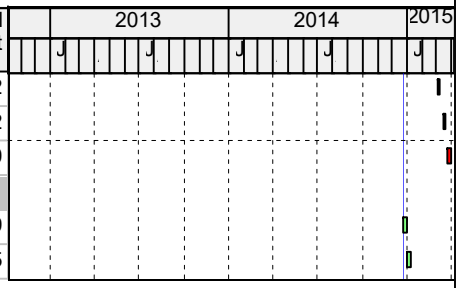



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Working Schedule - 1-26-15 Update/Revision** | | | | | | |
| L09-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-04 A | 30-Sep-14 A | |
| I-4500 | Re-design building exterior (change from EIFS panels | 30 | 0 | 12-Apr-13 A | 28-May-14 A | |
| I-1500 | Owner release revised LV design - Tower (ASIs 5, 13, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-1550 | Owner release revised LV design - Podium (ASIs 5, 1 | 200 | 0 | 23-May-13 A | 28-Apr-14 A | |
| I-1900 | Owner issue design revisions (ASIs 4, 9, 19, 34) | 215 | 0 | 23-May-13 A | 24-Mar-14 A | |
| I-2500 | Owner issue LL1 electrical revisions (ASIs 7, 9r2, 14, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-3400 | Owner provide Level 2 ceiling heights | 180 | 0 | 24-Jun-13 A | 24-Mar-14 A | |
| I-3700 | Owner resolve wall condition between stair and Eleva | 200 | 0 | 27-Jun-13 A | 16-Jun-14 A | |
| MM-1000 | MM - Temporary Power Available | 0 | 0 | 08-Jul-13 A | | |
| I-2100 | Owner revise roof steel design (Submittals 365, 370, | 200 | 0 | 09-Jul-13 A | 07-Apr-14 A | |
| I-2200 | Owner resolve elevator steel issue (RFI 112, RFI 112. | 200 | 0 | 09-Jul-13 A | 03-Mar-14 A | |
| I-2400 | Owner provide Tower light fixture selections (ASI 36) | 185 | 0 | 18-Jul-13 A | 08-Apr-14 A | |
| I-2900 | Owner revise Food Service and Kitchen (ASIs 11, 12, | 140 | 0 | 08-Aug-13 A | 27-Feb-14 A | |
| I-1400 | Owner develop envelope redesign | 70 | 0 | 27-Aug-13 A | 12-Dec-13 A | |
| I-3600 | Owner closeout glass/glazing allowance | 160 | 0 | 04-Sep-13 A | 30-Apr-14 A | |
| I-1200 | Owner release revised Concierge Lounge design (AS | 160 | 0 | 06-Sep-13 A | 08-Apr-14 A | |
| I-2800 | Owner revise interior public space design (ASIs 16, 1 | 130 | 0 | 25-Sep-13 A | 09-Apr-14 A | |
| I-2000 | Owner approve door frames (Submittals 258, 454, 48 | 85 | 0 | 27-Sep-13 A | 23-Jan-14 A | |
| I-3100 | Owner revise ballroom ceiling design (ASIs 18, 25) | 100 | 0 | 17-Oct-13 A | 25-Feb-14 A | |
| I-1600 | Owner provide directive for south & east corridor encl | 110 | 0 | 28-Oct-13 A | 18-Apr-14 A | |
| I-2300 | Owner resolve fire smoke dampers issue (RFI 233) | 115 | 0 | 30-Oct-13 A | 11-Apr-14 A | |
| I-2600 | Owner resolve L2 slab coordination issue | 4 | 0 | 13-Nov-13 A | 16-Nov-13 A | |
| I-2700 | Owner revise tower guest rooms design (ASIs 23, 29) | 58 | 0 | 04-Dec-13 A | 26-Feb-14 A | |
| I-1700 | Owner provide design for dry site utilities (ASIs 20, 20 | 66 | 0 | 09-Dec-13 A | 13-Mar-14 A | |
| I-1402 | Begin exterior panel production | 41 | 0 | 13-Dec-13 A | 12-Feb-14 A | |
| I-1300 | Owner issue "Hold" directive (email) | 0 | 0 | | 19-Dec-13 A | |

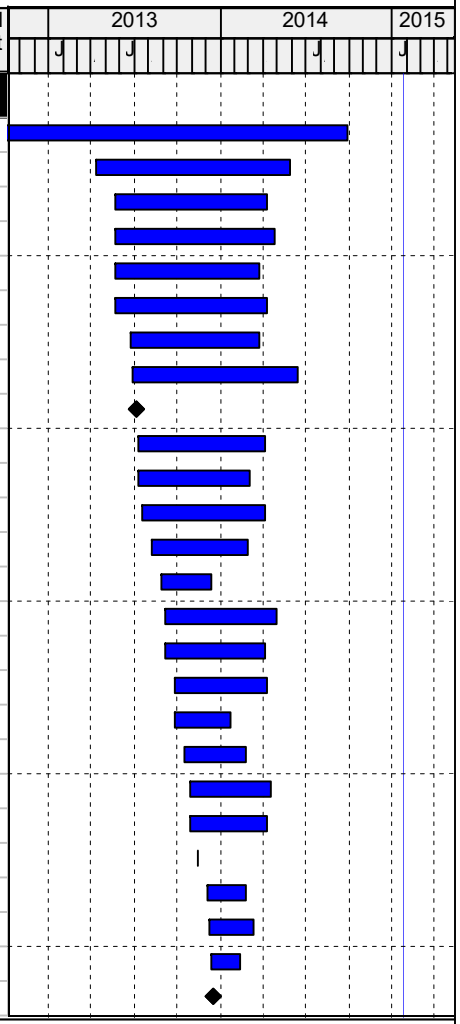


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1100 | Owner release revised L17 design (ASI 23, 29R1) | 74 | 0 | 20-Dec-13 A | 08-Apr-14 A | |
| I-1302 | Owner issue ASI 30 (Prep Kitchen Revisions) | 47 | 0 | 20-Dec-13 A | 27-Feb-14 A | |
| I-1404 | City of Bellevue Approval | 90 | 0 | 23-Dec-13 A | 15-Jul-14 A | |
| I-5470 | Resolve ceiling height issue at Laundry Room (RFI __ | 5 | 1 | 05-Jan-14 A | 26-Jan-15 | 18 |
| I-3000 | Owner revise bar area (change to straight bar, IDRFI-( | 71 | 0 | 22-Jan-14 A | 27-May-14 A | |
| I-1306 | Prep Kitchen - Additional plumbing (ASI 30) | 4 | 0 | 17-Feb-14 A | 01-Aug-14 A | |
| I-2202 | Fabricate revised elevator steel | 60 | 0 | 04-Mar-14 A | 07-May-14 A | |
| I-2704 | Framing "Go Back" work for ASIs 23, 29 - L4 | 1 | 0 | 05-Mar-14 A | 12-Mar-14 A | |
| I-3900 | RFI 471, Resolve Ballroom parapet height issue | 1 | 0 | 08-Mar-14 A | 07-May-14 A | |
| I-1702 | Owner provide directive to proceed | 26 | 0 | 14-Mar-14 A | 01-May-14 A | |
| I-3300 | Owner provide Guest Room plumbing fixture selectio | 1 | 0 | 20-Mar-14 A | 20-Mar-14 A | |
| I-1902 | Procure revised structural steel | 15 | 0 | 25-Mar-14 A | 14-Apr-14 A | |
| I-4000 | Owner complete design of east stitched enclosure (fo | 1 | 0 | 01-Apr-14 A | 14-May-14 A | |
| I-2102 | Fabricate revised roof steel | 20 | 0 | 08-Apr-14 A | 15-May-14 A | |
| I-3200 | Owner provide light fixture selections for podium level | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| I-3800 | Resolve  Heat Pump Electrical Overcurrent Issue | 20 | 0 | 23-Apr-14 A | 18-Jun-14 A | |
| L10-8221 | HVAC Risers Duct Insulation | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L11-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| I-2304 | Framing "Go Back" work at L3 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2306 | Framing "Go Back" work at L4 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2308 | Framing "Go Back" work at L5 for RFI 233 | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2706 | Framing "Go Back" work for ASIs 23, 29 - L5 | 1 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2708 | Framing "Go Back" work for ASIs 23, 29 - L6 | 1 | 0 | 29-Apr-14 A | 09-May-14 A | |
| I-2702 | Framing "Go Back" work for ASIs 23, 29 - L3 | 1 | 0 | 01-May-14 A | 01-May-14 A | |
| I-1706 | PSE scheduling delay | 10 | 0 | 01-May-14 A | 20-May-14 A | |
| I-3602 | Complete shop drawings & fab/deliver storefront fram | 40 | 0 | 01-May-14 A | 14-Jun-14 A | |

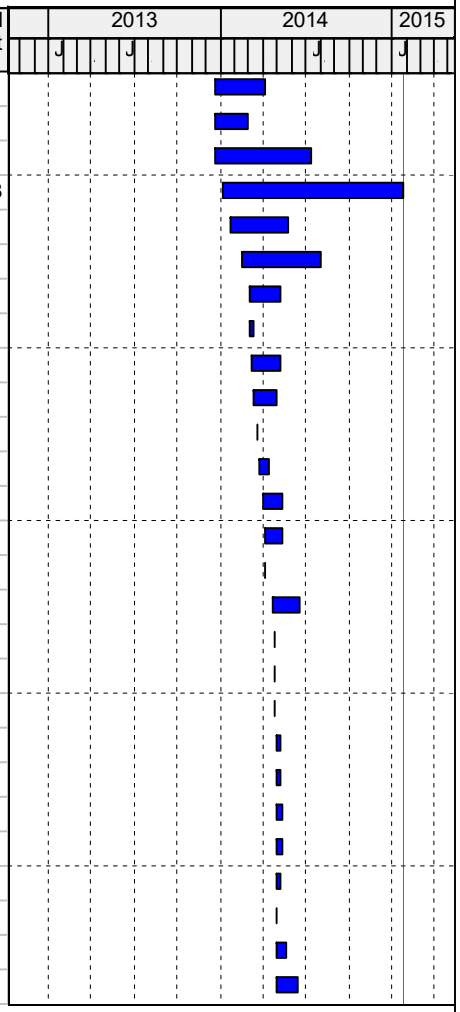


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| I-1802 | Rework framing for door hold-opens - LL4 | 1 | 0 | 07-May-14 A | 08-May-14 A | |
| L04-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-May-14 A | 12-May-14 A | |
| I-1800 | Owner issue directive to proceed with door hold-open | 1 | 0 | 08-May-14 A | 08-May-14 A | |
| I-1804 | Rework framing for door hold-opens - LL3 | 1 | 0 | 08-May-14 A | 09-May-14 A | |
| I-2312 | Framing "Go Back" work at L7 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-2314 | Framing "Go Back" work at L8 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-3902 | Install Ballroom parapet extension | 5 | 0 | 08-May-14 A | 13-May-14 A | |
| I-1806 | Rework framing for door hold-opens - LL2 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-1808 | Rework framing for door hold-opens - LL1 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-2310 | Framing "Go Back" work at L6 for RFI 233 | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| I-2710 | Framing "Go Back" work for ASIs 23, 29 - L7 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| L05-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L06-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L05-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| LL2E-8110 | LL2 - Electrical, Fire pumps/equipment final connectic | 5 | 0 | 12-May-14 A | 30-Oct-14 A | |
| PH-8704 | PH - Install Machine Support Steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| PH-8710 | Install elevator rail support steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| L03-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L03-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 13-May-14 A | 14-May-14 A | |
| I-4002 | East Stitched - Install framing and windows | 9 | 0 | 19-May-14 A | 09-Jun-14 A | |
| L10-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L11-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L12-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| RF-4038 | AR - Concrete pads and curbs | 5 | 0 | 21-May-14 A | 04-Jun-14 A | |
| L10-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |

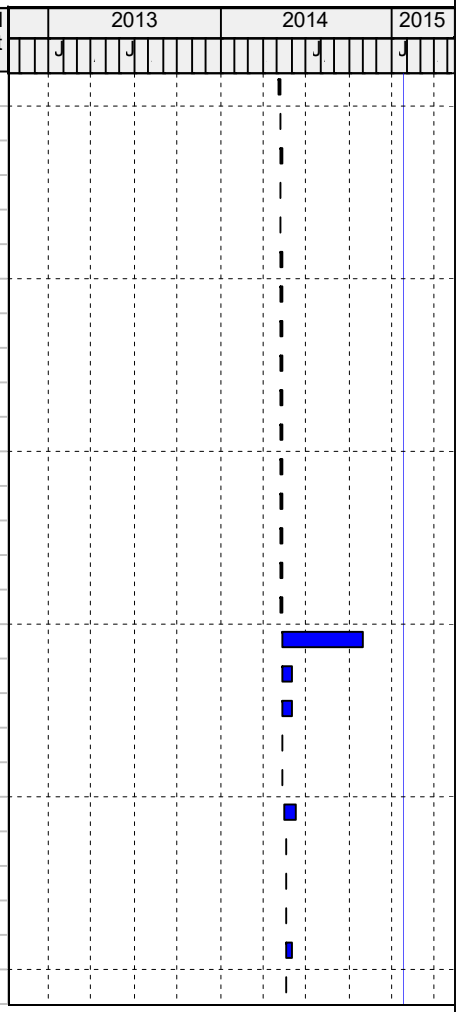



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L12-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L14-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L15-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 27-May-14 A | |
| L11-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 07-Jun-14 A | |
| L12-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 27-May-14 A | 06-Jun-14 A | |
| I-3002 | City of Bellevue approve bar design changes. | 5 | 0 | 28-May-14 A | 12-Dec-14 A | |
| I-4502 | Release metal panels for fabrication | 0 | 0 | 28-May-14 A | | |
| I-4504 | Metal panel fabrication (1st delivery) | 1 | 0 | 29-May-14 A | 08-Jul-14 A | |
| L16-8221 | HVAC Risers Duct Insulation | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| PH-8712 | PH - Complete Framing and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| PH-8714 | Stage PH/L18 roofing materials | 2 | 0 | 30-May-14 A | 30-May-14 A | |
| L08-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L08-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 02-Jun-14 A | 20-Jun-14 A | |
| PH-8704I | Correct support steel embeds | 2 | 0 | 02-Jun-14 A | 11-Jun-14 A | |
| L14-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 03-Jun-14 A | 04-Jun-14 A | |
| L17-8221 | HVAC Risers Duct Insulation | 1 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| PC-4010 | PC - Fireproof Entry Roof Steel | 5 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| I-4100 | Owner resolve trap primers issue (RFI 560) | 5 | 0 | 03-Jun-14 A | 20-Jun-14 A | |
| RF-6028 | Tower Roof - Structural Steel | 5 | 0 | 04-Jun-14 A | 17-Jun-14 A | |
| L14-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |

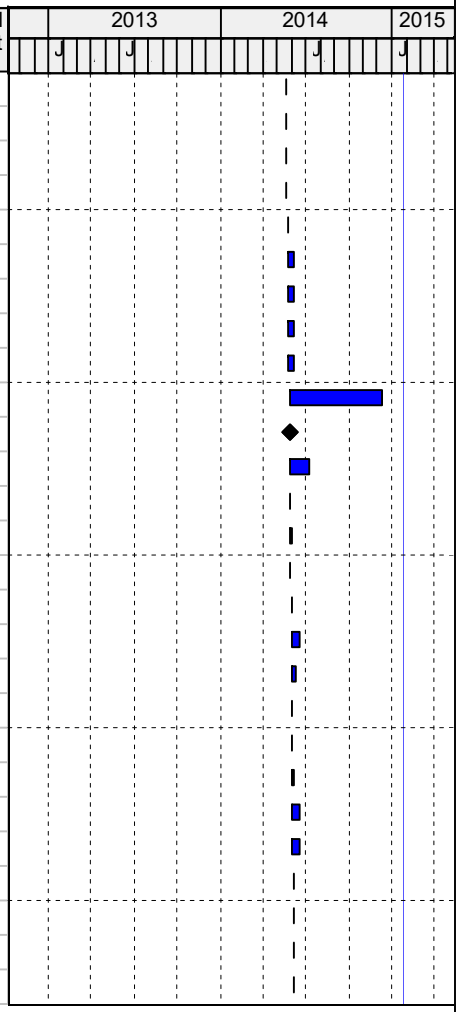



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L1B-6005 | Head of Wall Fire Caulk at CMU (including East Servi | 2 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L14-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L15-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L16-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L09-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 11-Jun-14 A | 12-Jun-14 A | |
| I-3702 | Complete wall framing at Stair/Elevator 5 (LL4) | 2 | 0 | 18-Jun-14 A | 20-Jun-14 A | |
| I-3720 | Fireproof added steel between Stair 1 and Elevator 5 | 5 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| I-3722 | Complete GWB between Stair 1 and Elevator 5 shaft | 10 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| LL1-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 22-Jul-14 A | |
| TC-5912 | Tower Crane pour-backs (LL4 to L3) | 4 | 0 | 19-Jun-14 A | 26-Jun-14 A | |
| LL1-Z2-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL4-6005 | LL4 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| LL3-6005 | LL3 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| L03-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 21-Jun-14 A | 21-Jun-14 A | |
| L06-6040 | Test Heat Pumps - L3, L4, L5 and L6 | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L03-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| L17-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL2-6005 | LL2 - Seismic Head Of Wall Fire Caulk at CMU | 5 | 0 | 24-Jun-14 A | 18-Jul-14 A | |
| I-3704 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL1-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z2-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z3-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 04-Aug-14 A | |
| L1L-6005 | Head of Wall Fire Caulk at CMU (including back of ho | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1K-6005 | Head of Wall Fire Caulk at CMU & Inspection | 2 | 0 | 24-Jun-14 A | 08-Aug-14 A | |
| L03-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L04-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |

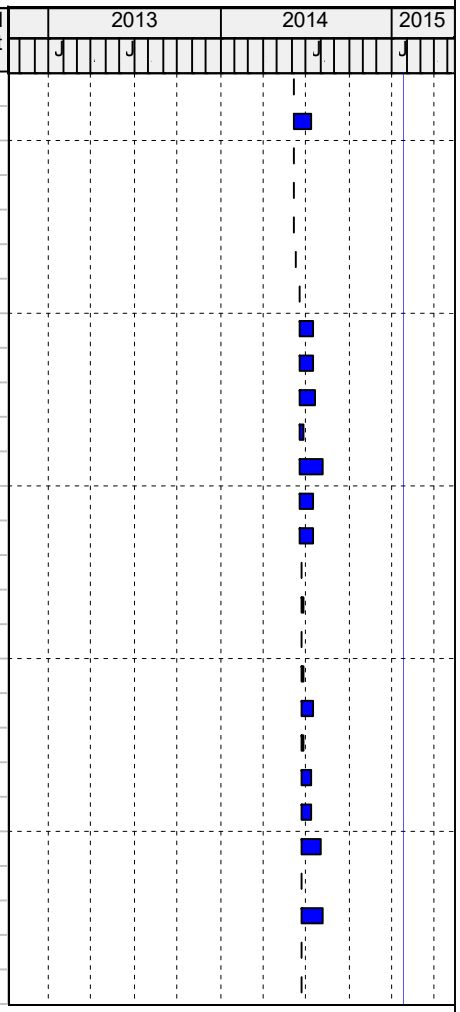



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| I-3710 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| I-3712 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| L1K-6018a | Install Kitchen hoods and grease ducts (OFCI) | 10 | 0 | 25-Jun-14 A | 07-Oct-14 A | |
| L03-8604 | L3 Pool - Plumbing R/I | 5 | 0 | 25-Jun-14 A | 10-Nov-14 A | |
| L04-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 26-Jun-14 A | 03-Jul-14 A | |
| L09-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 26-Jun-14 A | 26-Jun-14 A | |
| I-3706 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 26-Jun-14 A | 10-Jul-14 A | |
| L03-8600 | L3 Pool - Framing & HM frames | 5 | 0 | 26-Jun-14 A | 20-Nov-14 A | |
| L05-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L08-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L04-7018 | Electrical Rough-In | 1 | 0 | 27-Jun-14 A | 22-Jul-14 A | |
| L04-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 27-Jun-14 A | 23-Jul-14 A | |
| L03-7020 | HVAC Rough-In | 1 | 0 | 29-Jun-14 A | 15-Jul-14 A | |
| L1RR-8100 | Insulation [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8100 | Insulation [DELETED - included in Ballroom activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8100 | Insulation [DELETED - included in Meeting Rooms ac | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8102 | GWB Hang [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8215 | GWB Tape [DELETED - included in Meeting Rooms a | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8104 | Prime Paint [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |

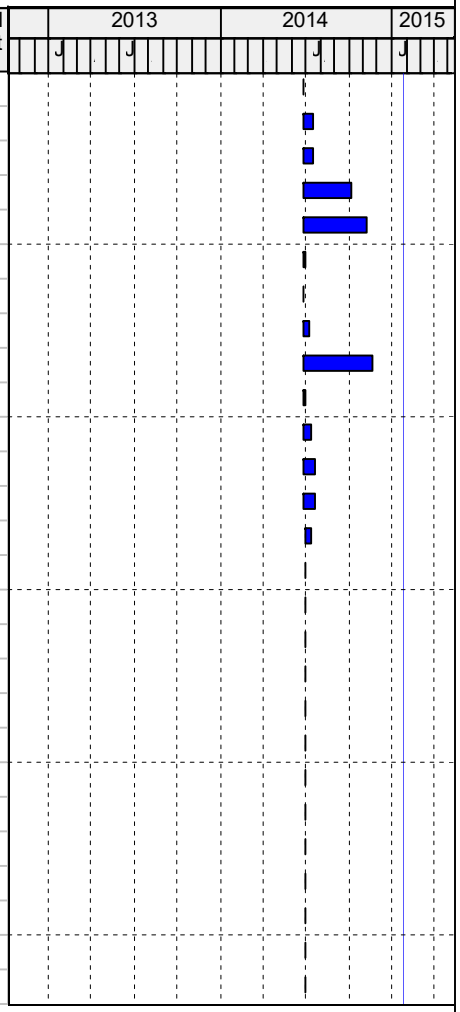


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z7-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8102 | GWB Hang [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8215 | GWB Tape [DELETED - included in Ballroom activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8104 | Prime Paint [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8102 | GWB Hang [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8215 | GWB Tape [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8104 | Prime Paint [DELETED - included in Kitchen activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L03-7018 | Electrical Rough-In | 1 | 0 | 01-Jul-14 A | 14-Jul-14 A | |
| L03-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Jul-14 A | 15-Jul-14 A | |
| L10-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7102 | Install Vertical Heat Pump | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L03-7116 | Frame Walls | 1 | 0 | 02-Jul-14 A | 14-Jul-14 A | |
| L03-7118 | Install HM Door Frame | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L04-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L05-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L07-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L08-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L09-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L10-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L12-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| I-3708 | Complete wall framing at Stair/Elevator 5 (LL3) | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |

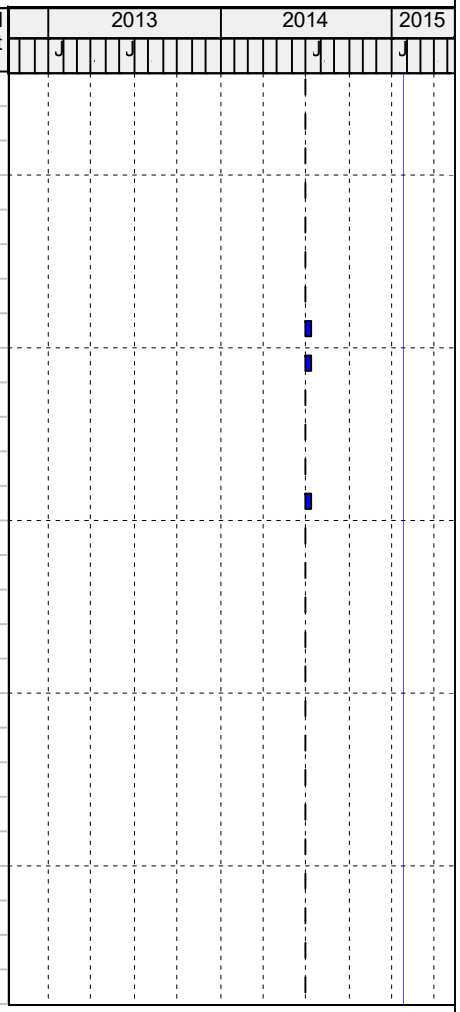



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L11-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 03-Jul-14 A | 07-Jul-14 A | |
| L04-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L05-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L06-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L07-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L08-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L17-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L10-6040 | Test Heat Pumps - L7, L8, L9 and L10 | 3 | 0 | 07-Jul-14 A | 09-Jul-14 A | |
| L10-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L03-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L04-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L05-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L06-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L07-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L08-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L09-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L10-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |

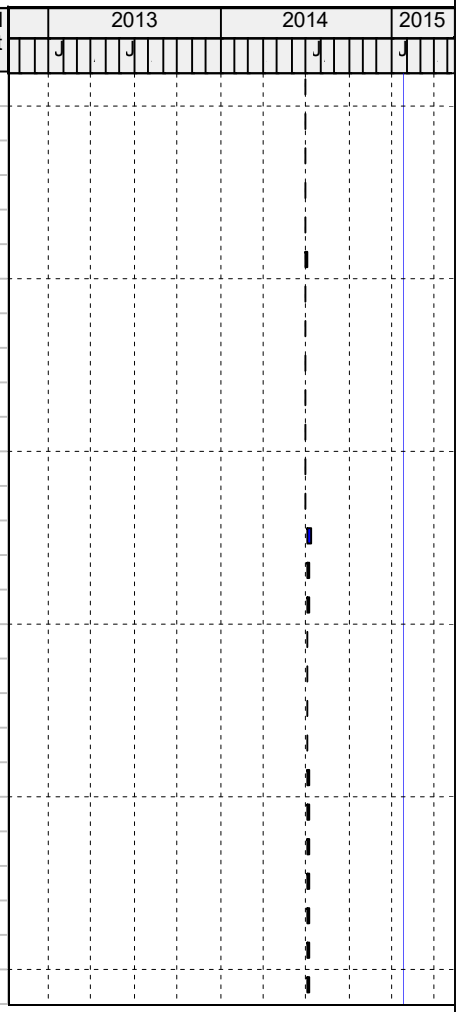



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L12-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L14-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L11-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Jul-14 A | 29-Jul-14 A | |
| L03-8602 | L3 Pool - Fire Sprinkler R/I | 5 | 0 | 08-Jul-14 A | 22-Jul-14 A | |
| L03-7016 | Install HM door frame | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L11-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L16-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 09-Jul-14 A | |
| L04-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |

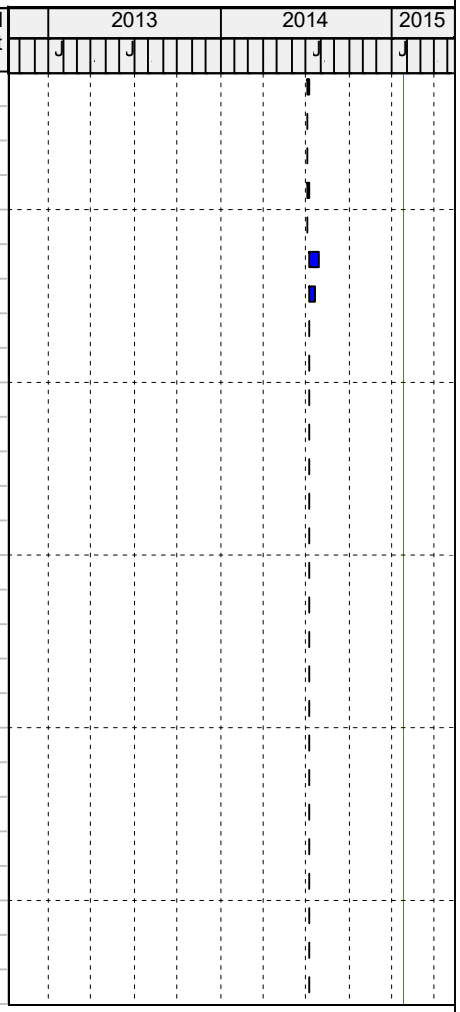



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L12-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| MP-FAB1 | Fabricate and Deliver Bronze Gold Horizontal Panels | 30 | 0 | 09-Jul-14 A | 15-Jul-14 A | |
| L04-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L05-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L06-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L16-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| MP-FAB2 | Fabricate and Deliver Silver Vertical Panels | 45 | 0 | 10-Jul-14 A | 25-Aug-14 A | |
| I-3004 | Issue ASI 38 | 0 | 0 | 11-Jul-14 A | | |
| I-3006 | Release bar area for x-ray examination | 5 | 0 | 11-Jul-14 A | 03-Sep-14 A | |
| L07-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| LL1-Z2-6018a | Complete Mech RI at tower crane opening (LL1) | 4 | 0 | 14-Jul-14 A | 17-Jul-14 A | |
| L08-6223 | Frame Corridor Ceilings | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| SW-2006a | Complete Dry Utilities (Phase 2) | 5 | 0 | 14-Jul-14 A | 24-Jul-14 A | |
| L04-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L04-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |

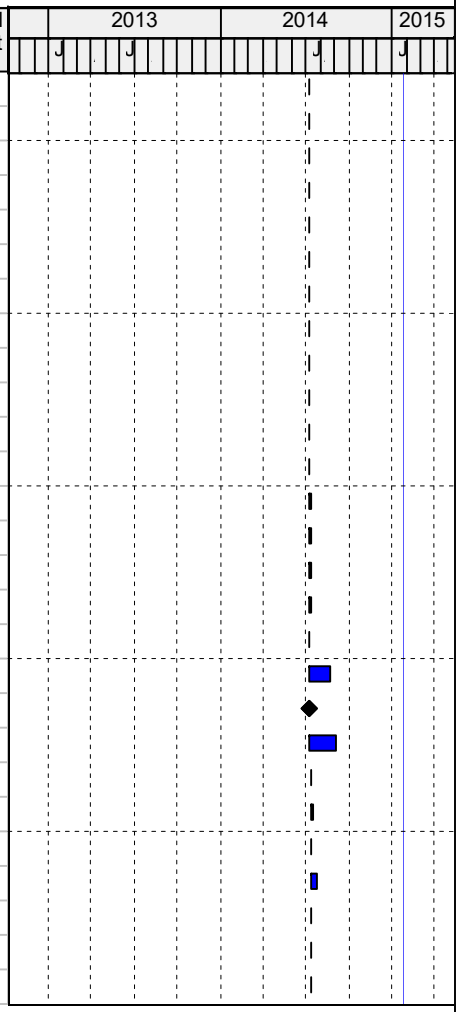



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L06-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L04-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L11-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L11-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L12-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L12-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L15-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |

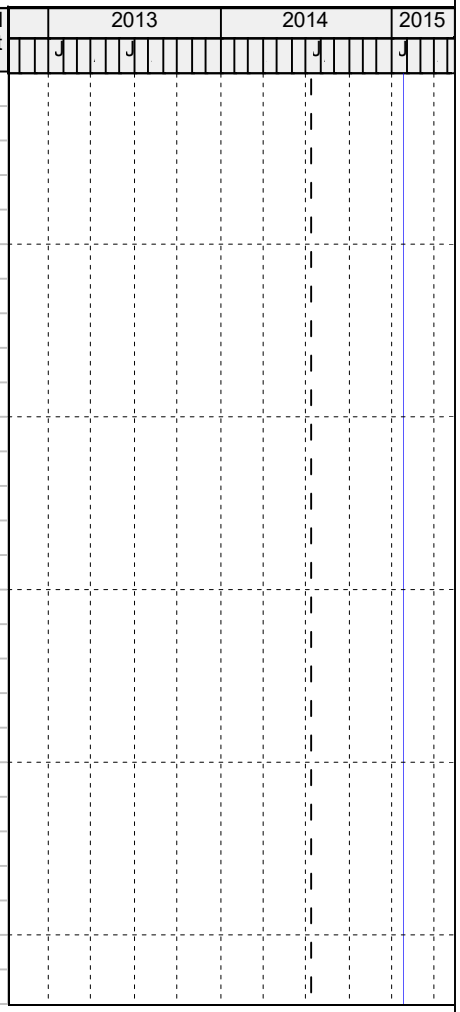



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-7102 | Install Vertical Heat Pump | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L1B-6026 | Install operable partition steel | 2 | 0 | 15-Jul-14 A | 08-Aug-14 A | |
| L09-6223 | Frame corridor ceilings | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L03-7120 | Electrical Rough-In | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L07-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L07-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L08-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L08-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L09-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L09-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L03-7142 | Install Laundry Chute (All Levels) | 9 | 0 | 15-Jul-14 A | 25-Jul-14 A | |
| LL2-2045 | LL2 - Electrical Room build-out | 15 | 0 | 15-Jul-14 A | 26-Sep-14 A | |
| L03-7122 | HVAC Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L04-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L05-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L06-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L07-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L07-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L08-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L08-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L09-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L09-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |

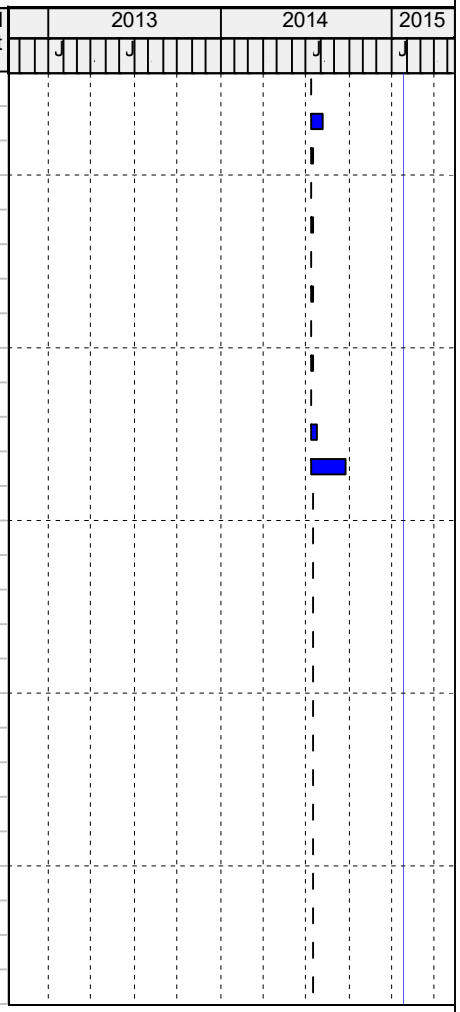



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L11-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L11-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L12-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L12-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L15-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L15-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L16-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L17-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L04-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L04-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L05-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L05-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L06-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L06-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L07-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L08-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |

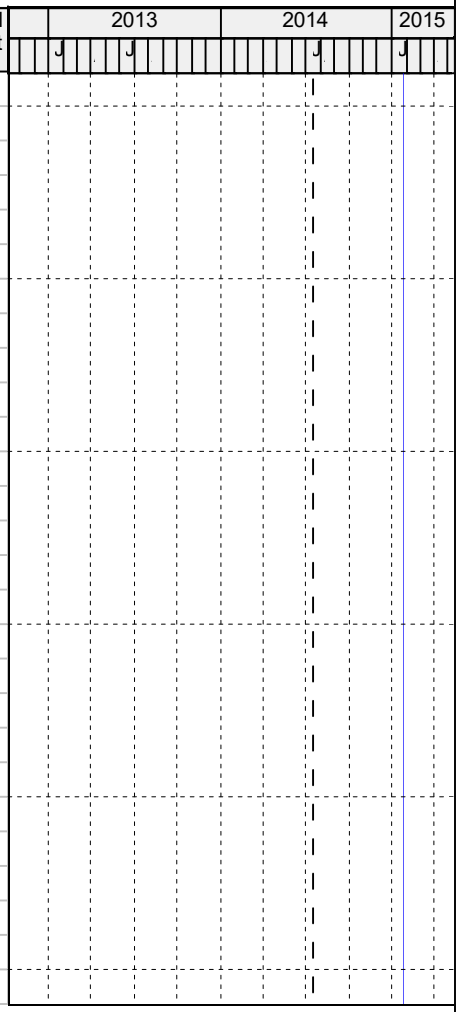



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L09-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L11-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L11-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L12-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L12-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L16-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L03-8608 | L3 Pool - Electrical R/I | 5 | 0 | 18-Jul-14 A | 10-Nov-14 A | |
| L03-8610 | L3 Pool - Fire Alarm / Elec Specialties R/I | 5 | 0 | 18-Jul-14 A | 10-Nov-14 A | |
| L15-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L15-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| L17-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L17-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| LL2-2052 | LL2 - Install fuel piping and exhaust duct to Generatc | 8 | 0 | 21-Jul-14 A | 15-Aug-14 A | |
| L04-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L04-7016 | Install HM door frame | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L07-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |

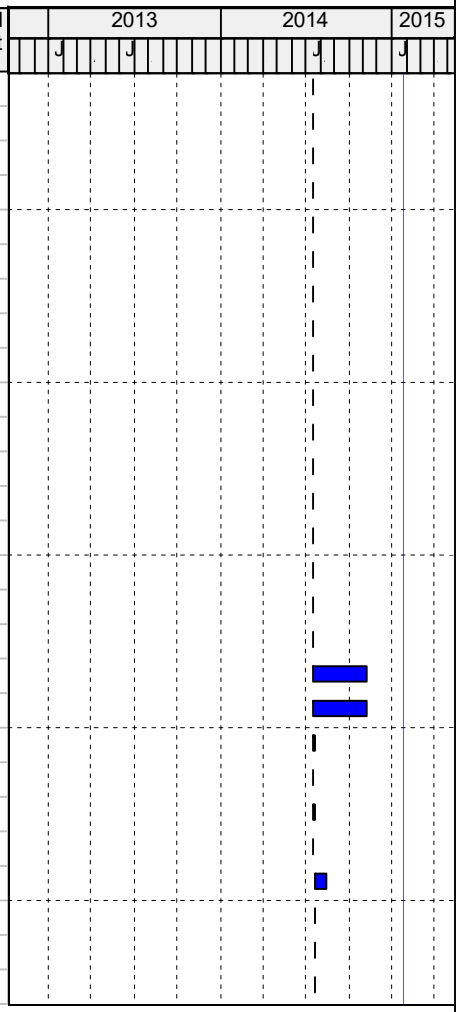


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L10-7116 | Frame Walls | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L16-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 21-Jul-14 A | 22-Jul-14 A | |
| L16-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L17-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| MPT-1002 | Tower - Install Elevation 35 (east elevation-south half) | 8 | 0 | 25-Jul-14 A | 04-Aug-14 A | |
| L16-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 25-Jul-14 A | 25-Jul-14 A | |
| L11-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L14-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L15-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L16-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L10-6223 | Frame Corridor Ceilings | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L11-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L15-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L15-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L11-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L14-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L16-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| I-1304 | Prep Kitchen - Additional framing (ASI 30) | 2 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-2302 | Framing "Go Back" work at LL1 for RFI 233 | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| I-2502 | Electrical rework at LL1 for ASIs 7, 9r2, 14, 27 | 4 | 0 | 01-Aug-14 A | 08-Aug-14 A | |

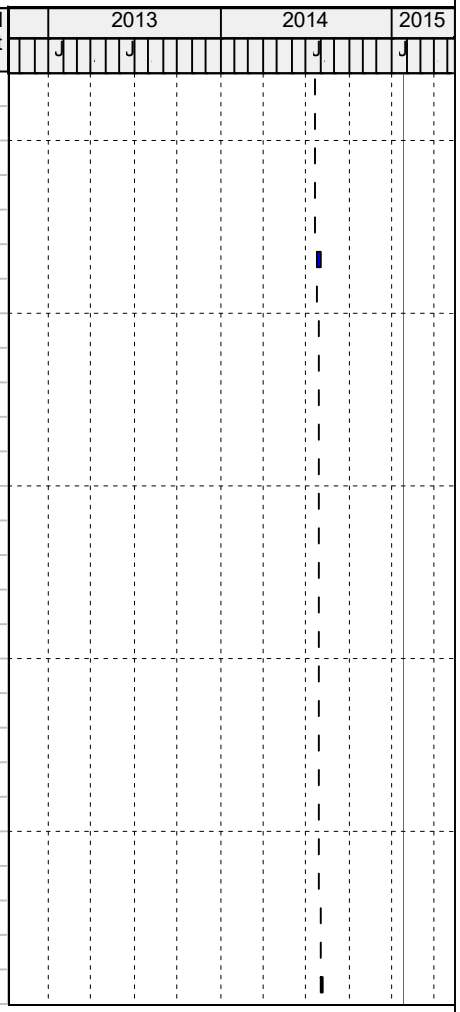



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L1B-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 01-Aug-14 A | 15-Aug-14 A | |
| MPL4-1000 | Upper L4 Ballroom - Install Elevations 1, 2 & 3 (south | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1000 | Tower - Install Elevations 26-27 (west elevation) [DELI | 13 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPP-1002 | Podium - Install Elevations 1 & 2 (west elevation, sou | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPP-1008 | Podium - Install Elevations 7 & 8 (north & east elevati | 9 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1002 | Upper L4 Ballroom - Install Elevation 10 (west elevatic | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1004 | Upper L4 Ballroom - Install Elevation 9 (north elevatio | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1006 | Tower - Install Elevation 40 (east return-east end) [DE | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1010 | Tower - Install Elevations 51 (north elevation) [DELET | 8 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-4004 | East Stitched - Install metal panels [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L11-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L11-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L15-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L14-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L17-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| MPT-1010b | Tower - Install Elevation 45 [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L16-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 04-Aug-14 A | 05-Aug-14 A | |
| L11-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Aug-14 A | 08-Aug-14 A | |
| L04-7020 | HVAC Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |

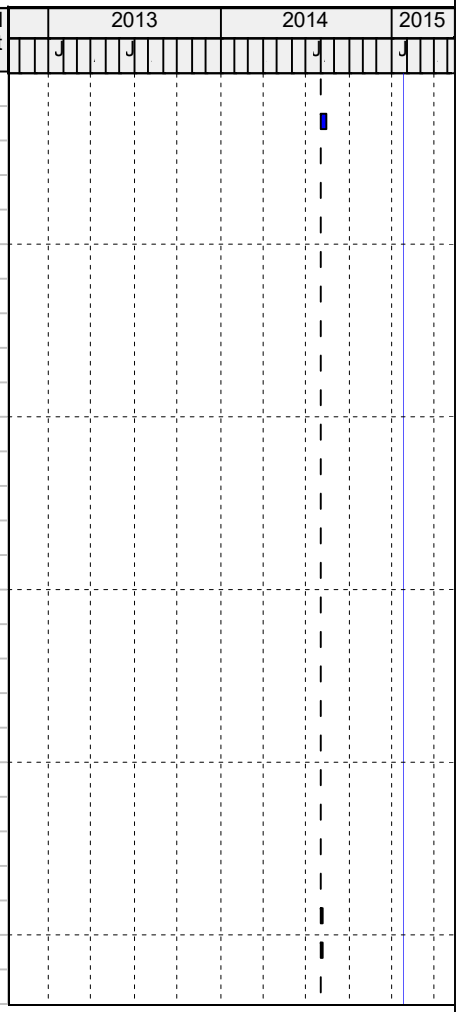



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L14-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L15-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 05-Aug-14 A | 07-Aug-14 A | |
| L05-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L06-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L07-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L08-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L09-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L10-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7018 | Electrical Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L14-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 05-Aug-14 A | 06-Aug-14 A | |
| L14-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| I-4104 | Install added trap primers - LL1 | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |

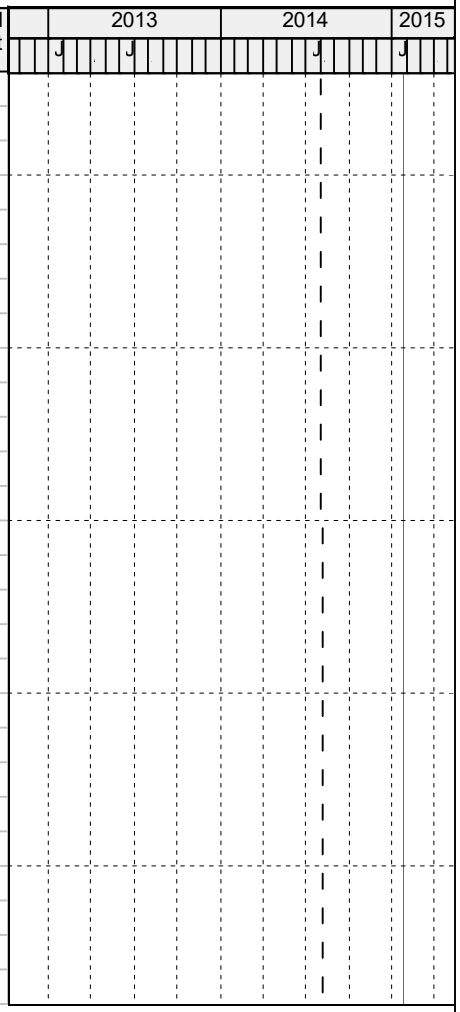



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L07-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L08-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L09-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L10-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7020 | HVAC Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L16-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| EL-1220 | Elevator fronts delivered | 0 | 0 | 07-Aug-14 A | | |
| L12-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L12-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-6223 | Frame Corridor Ceilings | 4 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L11-7016 | Install HM door frame | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L12-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L15-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L15-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L16-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L16-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |

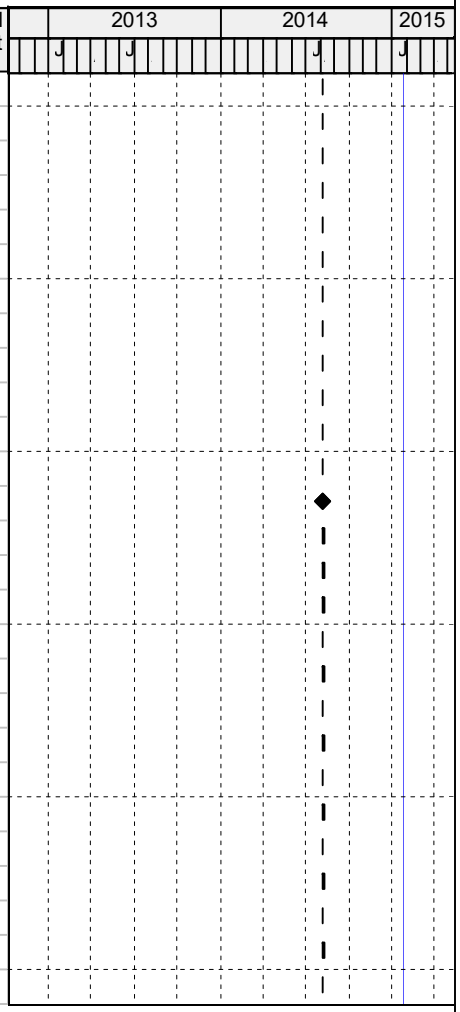



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L17-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-6040 | Test Heat Pumps - L11, L12 and L14 | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| PH-6026 | PH - Insulation/Vapor Barrier/GWB at Exterior Walls | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| L11-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L11-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-7026 | Inspections for GWB Cover | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 13-Aug-14 A | 13-Aug-14 A | |
| L15-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 14-Aug-14 A | 15-Aug-14 A | |
| LL2E-8108 | LL2 - Set fire pumps and equipment | 5 | 0 | 14-Aug-14 A | 29-Sep-14 A | |
| L10-7028 | GWB Hang/Tape/Finish | 5 | 0 | 14-Aug-14 A | 05-Dec-14 A | |
| L12-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L12-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L16-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L1BOH2-6008 | Int Wall Framing & Inspection | 5 | 0 | 14-Aug-14 A | 20-Aug-14 A | |
| I-4106 | Install added trap primers - L1 | 1 | 0 | 15-Aug-14 A | 15-Aug-14 A | |
| L14-6223 | Frame Corridor Ceilings | 4 | 0 | 15-Aug-14 A | 16-Aug-14 A | |

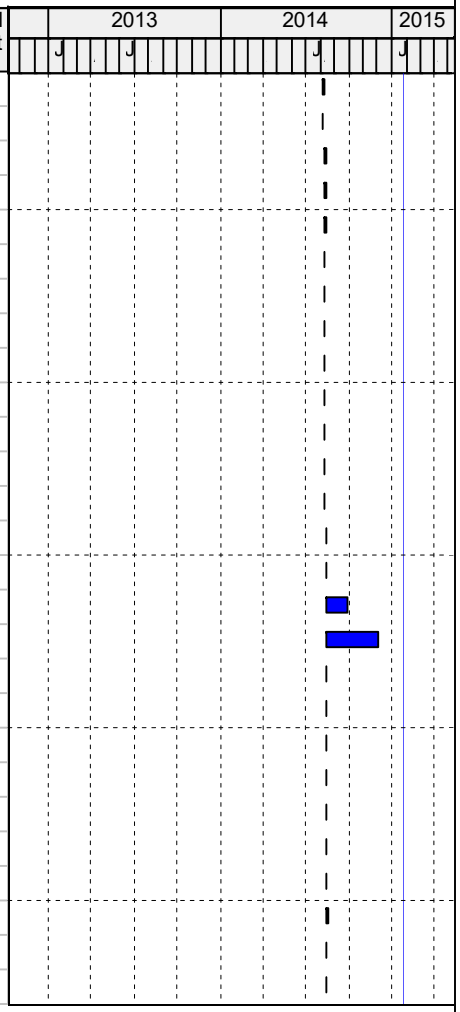


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8136 | Install Counter Subtops | 3 | 0 | 15-Aug-14 A | 18-Aug-14 A | |
| LL2-2054 | LL2 - GWB, Hang 1st Layer at Laundry Room | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| LL2E-8112 | LL2 - Form/Pour Fire Pump Pads/Curbs | 2 | 0 | 16-Aug-14 A | 18-Aug-14 A | |
| LL1-6014Ia | L1 bar redesign - rework plumbing at ceilings | 10 | 0 | 18-Aug-14 A | 05-Jan-15 A | |
| L15-6223 | Frame Corridor Ceilings | 4 | 0 | 18-Aug-14 A | 21-Aug-14 A | |
| L17-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Aug-14 A | 18-Aug-14 A | |
| L04-8136 | Install Counter Subtops | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-6014Ic | L1 bar redesign - rework electrical at ceilings | 10 | 0 | 18-Aug-14 A | 05-Jan-15 A | |
| LL2E-8114 | LL2 - Set Tube Steel at Door | 1 | 0 | 19-Aug-14 A | 19-Aug-14 A | |
| L17-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 20-Aug-14 A | 21-Aug-14 A | |
| L17-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 20-Aug-14 A | 20-Aug-14 A | |
| L05-8136 | Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 26-Aug-14 A | |
| L06-8136 | Bathrooms - Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 13-Oct-14 A | |
| L16-6223 | Frame Corridor Ceilings | 4 | 0 | 21-Aug-14 A | 29-Aug-14 A | |
| L17-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 21-Aug-14 A | 22-Aug-14 A | |
| L17-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 21-Aug-14 A | 21-Aug-14 A | |
| L1BOH2-6016 | Electrical RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6018 | HVAC RI | 4 | 0 | 21-Aug-14 A | 17-Oct-14 A | |
| L15-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7020 | HVAC Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7022 | Fire Sprinkler Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| LL2E-8116 | LL2 - Set Door Jamb | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |

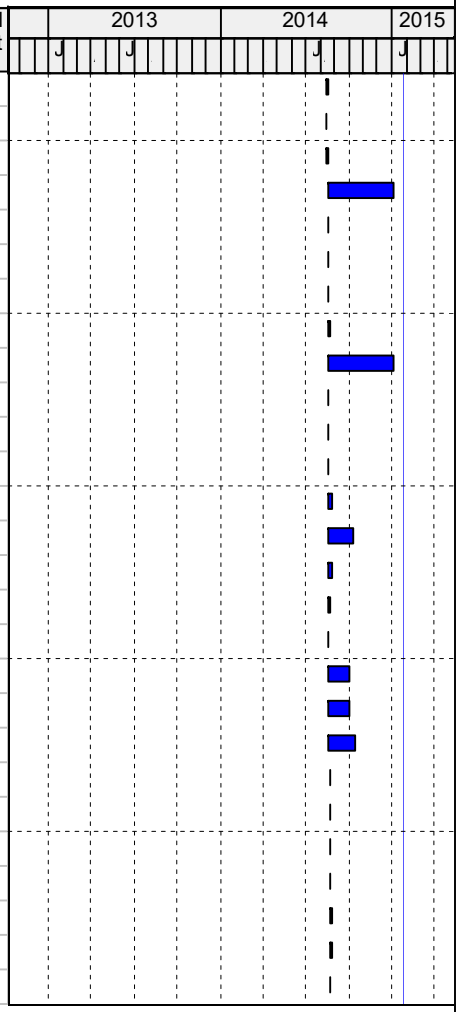



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7028 | GWB Hang/Tape/Finish | 5 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L05-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L05-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L06-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L06-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L03-8123 | Bathroom "Barn Doors" On Site | 0 | 0 | 25-Aug-14 A | | |

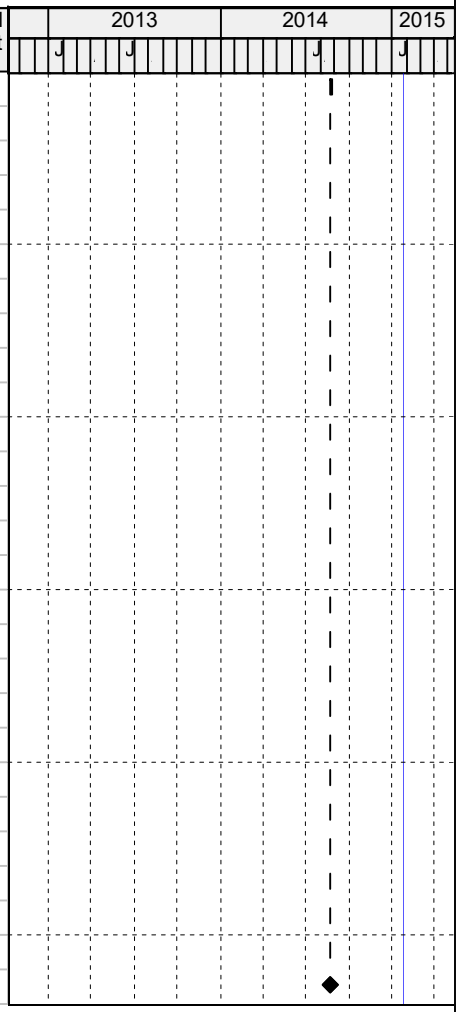



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-6026 | LL3 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL2-6026 | LL2 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL1-Z3-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L1BOH2-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L02-6026 | L2 - Set Elevator Fronts (Cars 1-4 | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L03-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L04-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L05-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L06-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L07-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L08-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L09-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L10-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L11-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L12-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L14-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L15-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L16-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L17-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| MPT-1008 | Tower - Install E/W Wing, N. Side West Half (Elev 50,: | 7 | 0 | 26-Aug-14 A | 03-Oct-14 A | |
| L06-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L07-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L08-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L05-7026 | Inspections for GWB Cover | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L05-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L11-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 08-Dec-14 A | |
| L12-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |

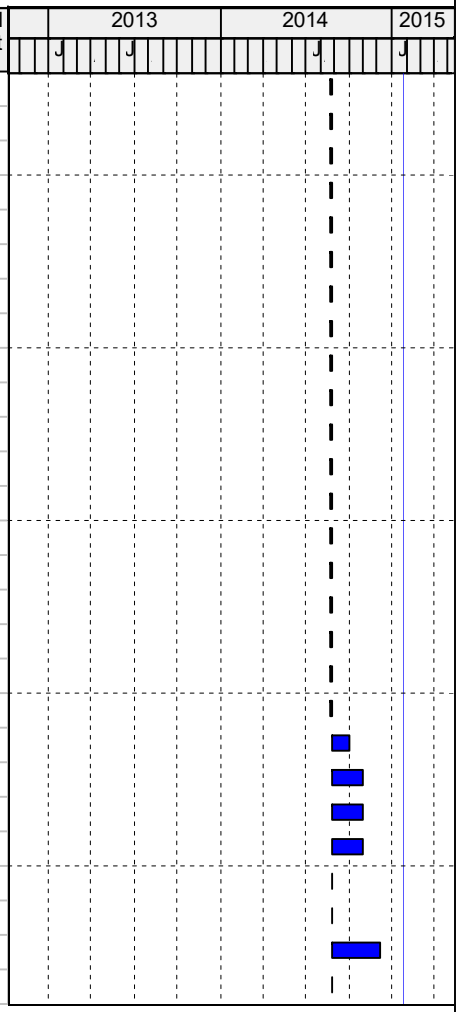



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L03-8105a | Painting - Split Door Jambs | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L09-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L10-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L11-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L12-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L14-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L15-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L16-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L05-8201 | Install ACT Grid @ Corridors | 2 | 0 | 27-Aug-14 A | 28-Aug-14 A | |
| L16-7022 | Fire Sprinkler Rough-In | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L04-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L06-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| EP-5110a | L1 - Install Steel at Revolving Door Opening | 3 | 0 | 27-Aug-14 A | 29-Aug-14 A | |
| L05-8105a | Painting - Split Door Jambs | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| I-4102 | Install added trap primers - LL2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4108 | Install added trap primers - L2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4110 | Install added trap primers - L3 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4112 | Install added trap primers - Roof PH | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| L03-8124d | Flooring On Site and Acclimated | 2 | 0 | 29-Aug-14 A | 01-Sep-14 A | |
| L02-5102 | L2 - Storefront Frames | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| L04-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L05-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L17-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L03-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L12-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L14-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |

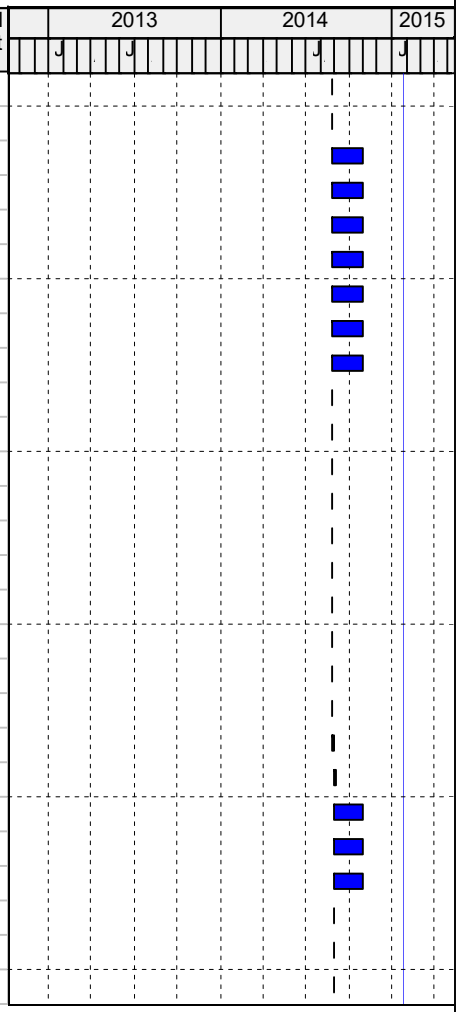



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8136 | Install Counter Subtops | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| LL1-Z3-FCC10 | FCC - Set Jamb | 1 | 0 | 02-Sep-14 A | 03-Sep-14 A | |
| MPT-1004 | Tower - Install E/W Wing, S. Side w/o Windows (Elev | 10 | 0 | 03-Sep-14 A | 17-Oct-14 A | |
| L03-7028 | GWB Hang/Tape/Finish | 5 | 0 | 03-Sep-14 A | 02-Dec-14 A | |
| L12-7028 | GWB Hang/Tape/Finish | 5 | 0 | 03-Sep-14 A | 08-Dec-14 A | |
| L03-8126a | Doors & Hardware On Site | 0 | 0 | 03-Sep-14 A | | |
| LL1-Z3-FCC12 | FCC - Sheetrock Outside Wall | 1 | 0 | 03-Sep-14 A | 03-Sep-14 A | |
| L16-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| L17-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Sep-14 A | 11-Sep-14 A | |
| L02-5104b | L2 - Install Storefront Temporary Enclosures | 1 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| LL1-Z3-FCC14 | FCC - Verify Fire Caulk OK & Inspect Room OK to 2n | 1 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| I-3008 | Coordinate and perform x-ray examination | 7 | 0 | 04-Sep-14 A | 12-Sep-14 A | |
| L02-5104a | L2 - Measure/Fabricate Storefront Glazing | 15 | 0 | 05-Sep-14 A | 18-Sep-14 A | |
| LL1-Z3-FCC16 | FCC - GWB, Hang 2nd Layer | 2 | 0 | 05-Sep-14 A | 08-Sep-14 A | |
| L03-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L15-7018 | Electrical Rough-In | 1 | 0 | 08-Sep-14 A | 08-Sep-14 A | |
| EL-1228 | Construct/Approve elevator lobby framing mockup (L | 3 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| LL2E-8118 | LL2 - Frame Infill, Install Densglass & Inspect at Fire I | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L06-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L08-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L15-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7018 | Electrical Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L3-5104a | L3 - Measure/Fabricate Storefront Glazing | 15 | 0 | 09-Sep-14 A | 30-Sep-14 A | |
| L03-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 23-Sep-14 A | |

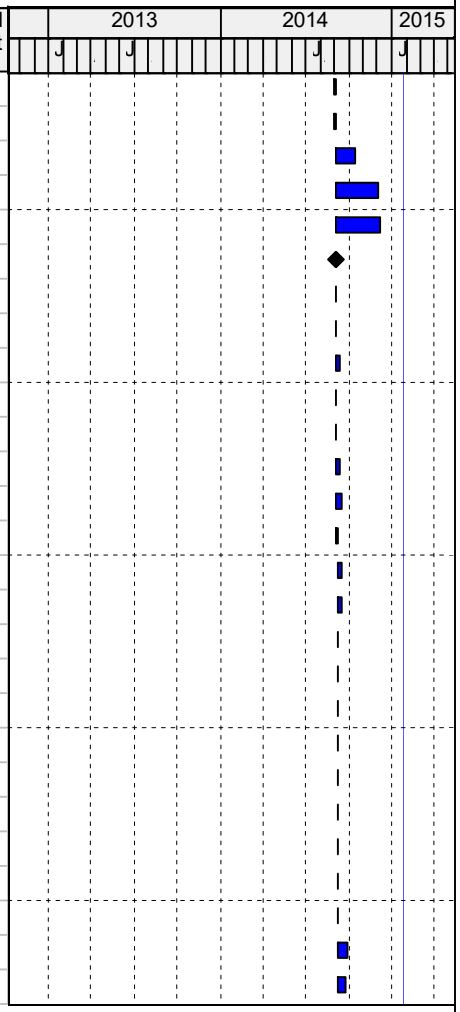


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L04-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L06-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| L08-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| L05-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L06-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L06-7028 | GWB Hang/Tape/Finish | 5 | 0 | 10-Sep-14 A | 02-Dec-14 A | |
| L08-7028 | GWB Hang/Tape/Finish | 5 | 0 | 10-Sep-14 A | 05-Dec-14 A | |
| L15-7026 | Inspections for GWB Cover | 1 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| LL2E-8120 | LL2 - Insulation, Vapor Barrier & Inspect at Fire Pump | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L08-8395 | Framing at Elevator Lobby | 4 | 0 | 11-Sep-14 A | 17-Sep-14 A | |
| L15-7028 | GWB Hang/Tape/Finish | 5 | 0 | 11-Sep-14 A | 08-Dec-14 A | |
| L08-8136 | Install Counter Subtops | 3 | 0 | 11-Sep-14 A | 16-Sep-14 A | |
| L02-6025 | L2 - Framing Go-Back Work (left out for mechanical e | 4 | 0 | 11-Sep-14 A | 02-Oct-14 A | |
| L1-5104a | L1 - Measure/Fabricate Storefront Glazing | 15 | 0 | 12-Sep-14 A | 18-Sep-14 A | |
| L1B-8102c | Finish framing and MEP at Main Ballroom East Wall ( | 10 | 0 | 12-Sep-14 A | 02-Oct-14 A | |
| L09-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L10-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L11-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L12-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L16-7026 | Inspections for GWB Cover | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| MPT-1014 | Tower - Install E/W Wing, N. Side, E. Half (Elev 46-49 | 8 | 0 | 15-Sep-14 A | 28-Oct-14 A | |
| LL2-6032 | LL2 - Complete Framing (Including Elevator Lobby) | 4 | 0 | 15-Sep-14 A | 18-Sep-14 A | |
| L1-5104b | L1 - Install Storefront Temporary Enclosures | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| LL1-Z3-FCC18 | FCC - Install Temp Door | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| LL2-2058a | LL2 - GWB Hang 1st Layer | 5 | 0 | 15-Sep-14 A | 19-Sep-14 A | |

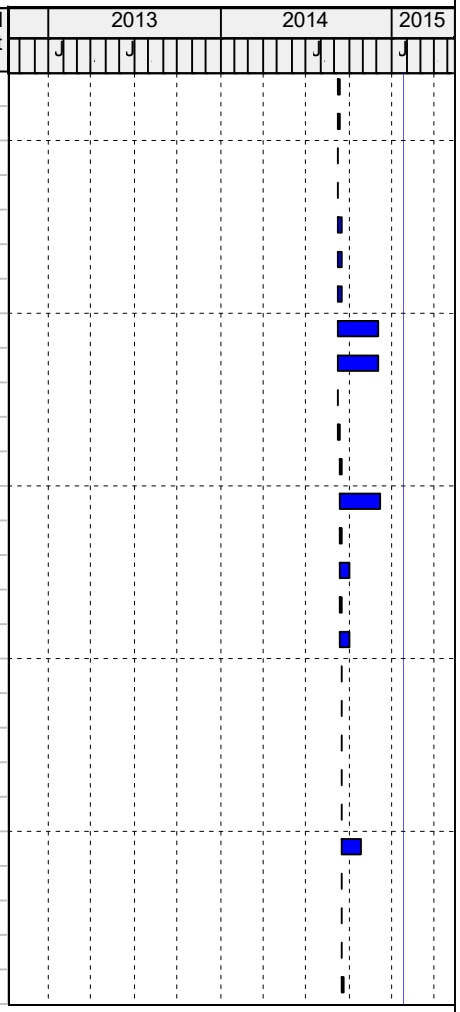



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2064 | LL2 - Generator Room - Finish Exhaust Piping | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| I-3010 | Prepare proposal for MEP relocations | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| L16-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L07-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L09-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L10-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L14-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L15-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L03-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| L16-7028 | GWB Hang/Tape/Finish | 5 | 0 | 16-Sep-14 A | 08-Dec-14 A | |
| L17-7018 | Electrical Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L09-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L10-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| LL3-6028 | LL3 - Frame Elevator Lobby | 2 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| LL4-6026 | LL4 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| I-3012 | Owner approve proposal for MEP relocations | 3 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| L11-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L12-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L14-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L15-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L04-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L17-7026 | Inspections for GWB Cover | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L17-7116 | Frame Walls | 4 | 0 | 17-Sep-14 A | 29-Sep-14 A | |
| LL2-2066 | LL2 - Generator Room - Finish Fuel Piping | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L16-8395 | Framing at Elevator Lobby | 4 | 0 | 18-Sep-14 A | 26-Sep-14 A | |
| L02-5104 | L2 - Storefront Glazing | 2 | 0 | 18-Sep-14 A | 22-Sep-14 A | |

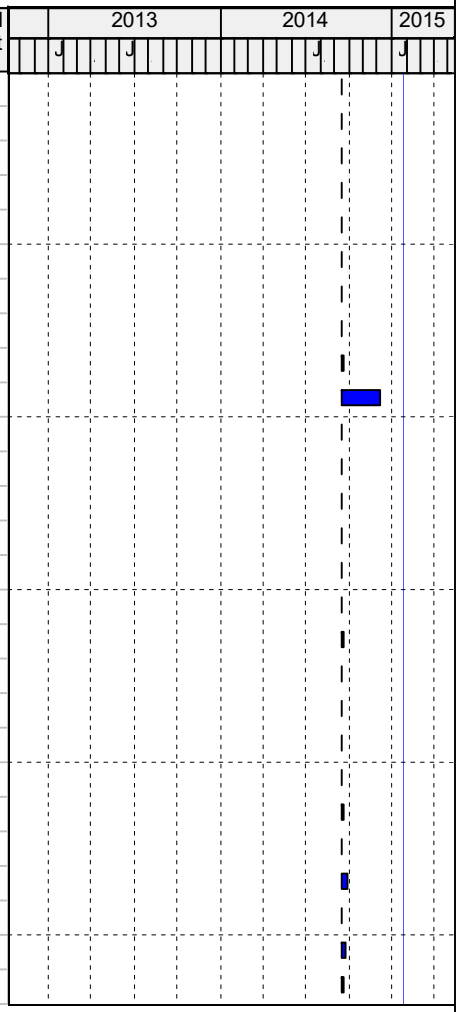



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7028 | GWB Hang/Tape/Finish | 5 | 0 | 18-Sep-14 A | 08-Dec-14 A | |
| LL4-6028 | LL4 - Frame Elevator Lobby | 2 | 0 | 18-Sep-14 A | 02-Oct-14 A | |
| MPT-1010a | Tower - Install E/W Wing, West End (Elev 52,53) | 8 | 0 | 18-Sep-14 A | 10-Oct-14 A | |
| LL2-2068 | LL2 - Generator Room - Electrical Finishes | 3 | 0 | 19-Sep-14 A | 30-Sep-14 A | |
| L07-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L09-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L04-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L05-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L03-8140 | Countertops On Site | 0 | 0 | 22-Sep-14 A | | |
| L03-8129a | Shower Doors On Site | 0 | 0 | 22-Sep-14 A | | |
| LL1-Z3-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L1BOH2-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2-2048a | LL2 - Move in Laundry Room Ironer | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2E-8122 | LL2 - Hang GWB at Fire Pump Room | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-FCC20 | FCC - Rough-In and Install Panels | 25 | 0 | 22-Sep-14 A | 21-Nov-14 A | |
| I-3014 | Core drill for MEP relocations | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L05-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L07-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 05-Dec-14 A | |
| L09-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 05-Dec-14 A | |
| L14-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 08-Dec-14 A | |
| L04-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L05-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L06-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L07-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L04-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |

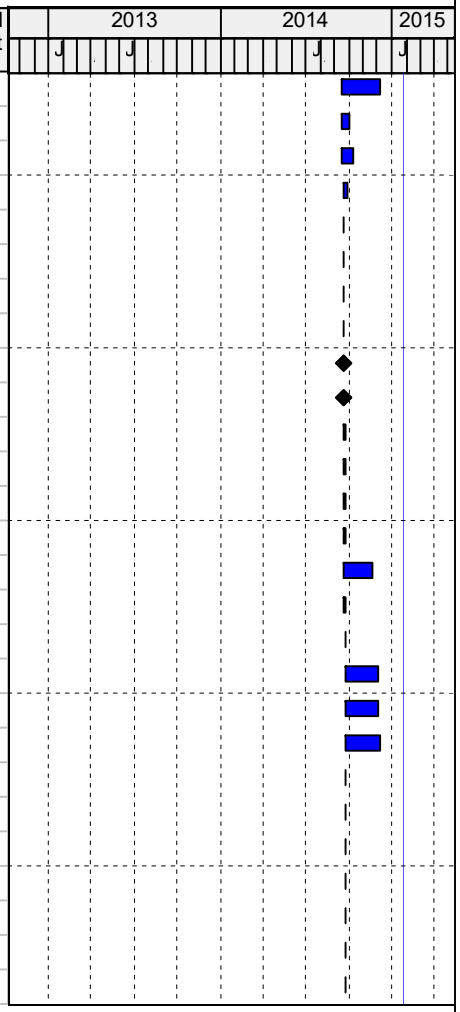


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L04-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L05-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-7122 | HVAC Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| LL2-2058 | LL2 - Tape/Finish Laundry Room | 3 | 0 | 24-Sep-14 A | 26-Sep-14 A | |
| L08-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L17-8395 | Framing at Elevator Lobby | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L05-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L06-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L07-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L08-7120 | Electrical Rough-In | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| LL2E-8124 | LL2 - Temp-In Louver Opening at Fire Pump Room | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L1-5104c | L1 - Install Storefront at Main Entry Facade | 5 | 0 | 25-Sep-14 A | 10-Oct-14 A | |
| L16-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L08-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L10-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L16-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L17-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L17-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |

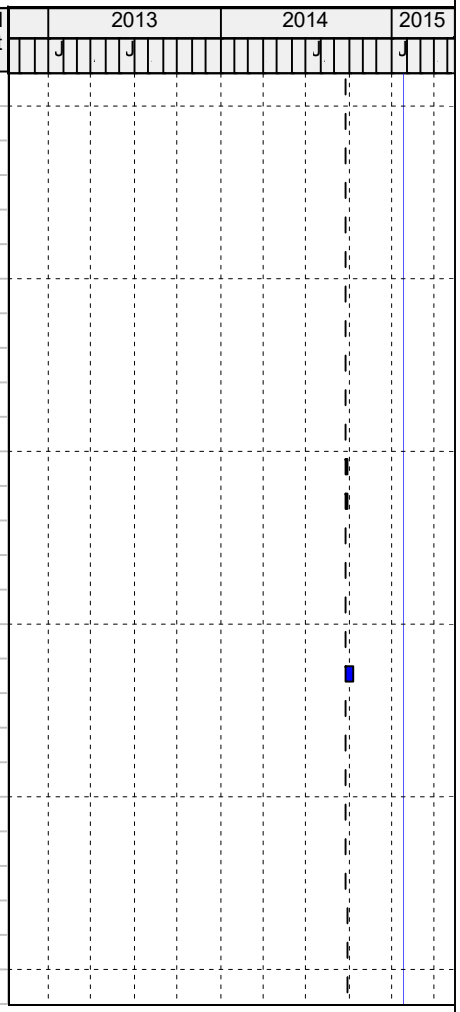



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L11-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L12-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L14-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L15-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L17-7118 | Install HM Door Frame | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| LL3-6030 | LL3 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL4-6030 | LL4 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL2-6034 | LL2 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L1BOH2-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L02-6030 | L2 - Framing at Elevator Lobby & North Half | 4 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| MPT-1022 | Tower - Caulking, west | 8 | 0 | 29-Sep-14 A | 03-Nov-14 A | |
| PH-6015 | PH - Set Boilers and Pumps | 12 | 0 | 29-Sep-14 A | 15-Oct-14 A | |
| L11-8204 | Bathrooms - Vinyl Wall Coverings | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L10-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L17-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L11-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L12-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L07-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 30-Sep-14 A | 08-Oct-14 A | |
| L11-8201 | Install ACT Grid @ Corridors | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L09-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L09-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L11-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |

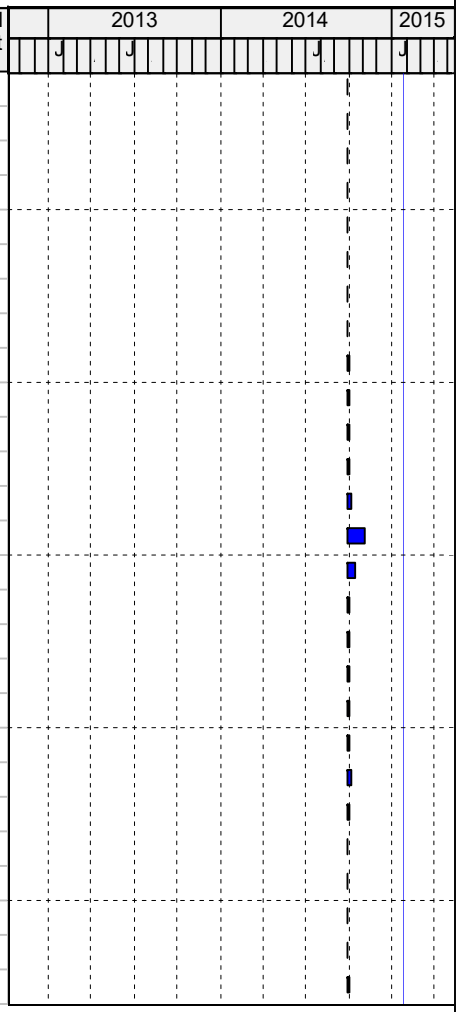



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L14-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L15-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| LL2-2072 | Generator - Complete generator and annunciator cor | 5 | 0 | 30-Sep-14 A | 21-Oct-14 A | |
| L17-6040 | Test Heat Pumps - L16 and L17 | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L17-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L14-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L03-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |

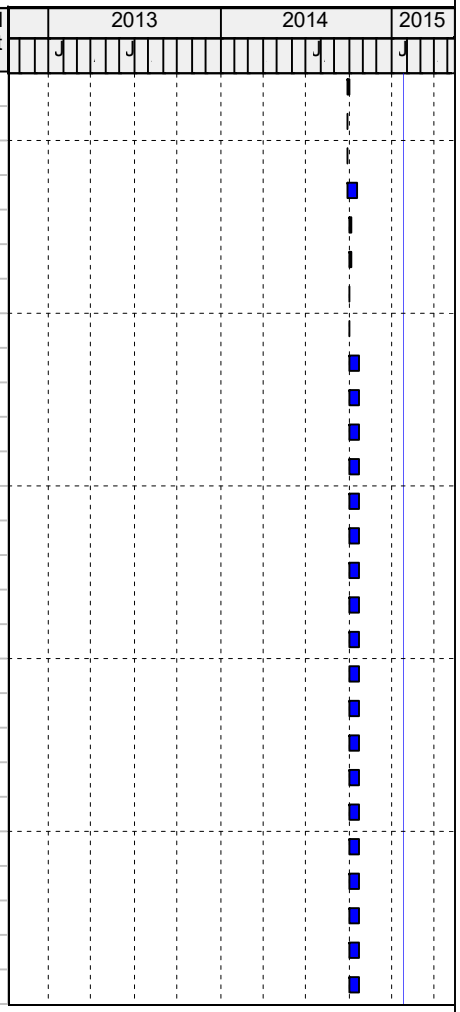


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L11-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L12-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L12-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L14-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L16-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L17-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L09-8136 | Install Counter Subtops | 3 | 0 | 01-Oct-14 A | 03-Oct-14 A | |
| L02-6032 | L2 - Electrical RI at Elevator Lobby & North Half | 5 | 0 | 01-Oct-14 A | 08-Oct-14 A | |

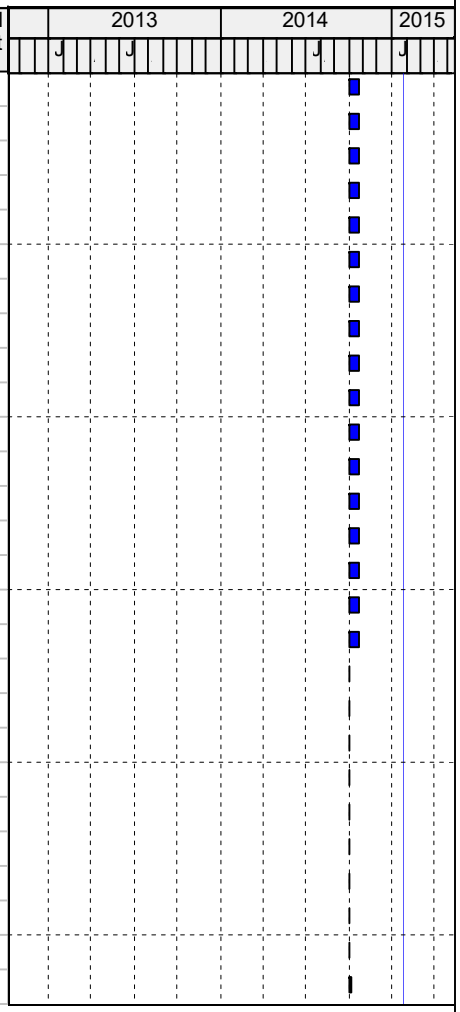


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2306 | Prep, grind and overlay at 11th Ave, 3rd Place & 2nd | 5 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 01-Oct-14 A | 16-Dec-14 A | |
| L16-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L14-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L15-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1BOH2-8130 | Inspections For Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L02-6024a | L2 - Inspections - South Half | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L06-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| L17-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| LL2-2074 | Generator - Install fuel fill | 2 | 0 | 03-Oct-14 A | 06-Oct-14 A | |
| L07-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| MPT-1020 | Tower - Install E/W Wing, East End (Elev 41,44) | 5 | 0 | 06-Oct-14 A | 18-Oct-14 A | |
| LL1-8102a | GWB Hang/Tape (Ceilings) | 10 | 0 | 06-Oct-14 A | 18-Nov-14 A | |
| L1BOH2C-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6014 | Complete Plumbing RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6016 | Complete Electrical RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6018 | Complete HVAC RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L03-8200a | New murals on site (date estimated) | 0 | 0 | 06-Oct-14 A | | |
| SW-2100 | Zone 1 - Survey curb & site lighting | 2 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 06-Oct-14 A | 06-Oct-14 A | |
| L1BOH2-8100 | Insulation | 4 | 0 | 07-Oct-14 A | 13-Oct-14 A | |

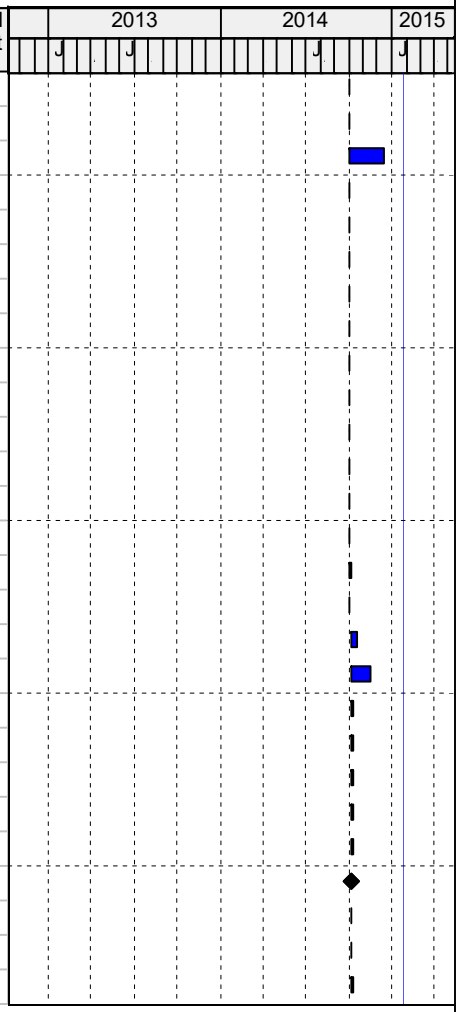


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L12-8201 | Install ACT Grid @ Corridors | 2 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| L10-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 07-Oct-14 A | 20-Oct-14 A | |
| L03-8216x | Vinyl Wall Coverings - Install Murals | 2 | 0 | 07-Oct-14 A | 29-Dec-14 A | |
| L1B-8102b | GWB Hang (Walls) & Inspection - Exterior Wall at Cor | 3 | 0 | 07-Oct-14 A | 09-Oct-14 A | |
| RF-4048 | Tower Roof - Install davit arms | 3 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| LL2-2076 | Generator - Install fuel fill mechanical piping | 4 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L12-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L09-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L03-8633 | Pool - Install waterproofing & test | 3 | 0 | 08-Oct-14 A | 17-Oct-14 A | |
| L03-8130 | Install Door Hardware | 3 | 0 | 08-Oct-14 A | 28-Oct-14 A | |
| L10-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L02-8102a | L2 - GWB Hang / Tape / Finish - South Half | 7 | 0 | 09-Oct-14 A | 27-Oct-14 A | |
| SW-2102 | Zone 1 - Vacate SE corner | 2 | 0 | 09-Oct-14 A | 11-Oct-14 A | |
| SW-2106 | Zone 1 - Sawcut and remove asphalt | 4 | 0 | 09-Oct-14 A | 14-Oct-14 A | |
| L11-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 09-Oct-14 A | |
| SW-2200 | Zone 2 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |
| SW-2300 | Zone 3 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |
| SW-2108 | Zone 1 - Install east footing drain | 4 | 0 | 10-Oct-14 A | 20-Oct-14 A | |
| L04-8130 | Install Door Hardware | 3 | 0 | 10-Oct-14 A | 29-Oct-14 A | |
| ML-5962 | Man/Material Lifts - Remove Roof Lift Stop | 0 | 0 | | 11-Oct-14 A | |
| I-1102 | Additional work at new L17 guest rooms | 5 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| LL2-2046 | LL2 - Generator Room - Misc. Finishes | 3 | 0 | 13-Oct-14 A | 21-Nov-14 A | |
| RF-4008 | Tower Roof - Install corrugated metal panels | 5 | 0 | 13-Oct-14 A | 03-Nov-14 A | |
| MPT-1018b | Tower - Roof cornice frame & sheath | 6 | 0 | 13-Oct-14 A | 24-Oct-14 A | |
| L02-8100a | L2 - Insulation - South Half | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| SW-2112 | Zone 1 - Grade for curb and gutter | 3 | 0 | 13-Oct-14 A | 17-Oct-14 A | |

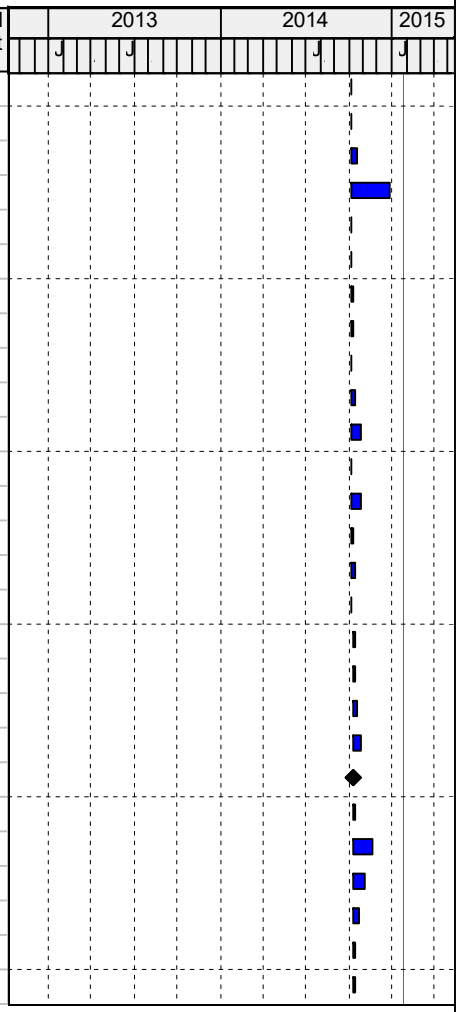



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2202 | Zone 2 - Install site lighting | 5 | 0 | 13-Oct-14 A | 24-Nov-14 A | |
| SW-2204 | Zone 2 - Repave utility trenches | 4 | 0 | 13-Oct-14 A | 22-Oct-14 A | |
| L12-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 13-Oct-14 A | |
| SW-2302 | Zone 3 - Grade for curb and gutter | 2 | 0 | 14-Oct-14 A | 01-Dec-14 A | |
| L14-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 14-Oct-14 A | 16-Oct-14 A | |
| L05-8130 | Install Door Hardware | 3 | 0 | 14-Oct-14 A | 03-Nov-14 A | |
| L14-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 14-Oct-14 A | |
| L16-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L15-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 15-Oct-14 A | 17-Oct-14 A | |
| L15-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 15-Oct-14 A | |
| SW-2206 | Zone 2 - Grade for curb and gutter | 2 | 0 | 16-Oct-14 A | 20-Oct-14 A | |
| MPP-1000 | Podium - Install W/S/N Elevations (Elev 1-5, 6,9-19,2 | 10 | 0 | 20-Oct-14 A | 10-Dec-14 A | |
| L06-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 20-Oct-14 A | 23-Oct-14 A | |
| LL2-8106a | LL2, Garage - Pinned Insulation (except at ramp) | 4 | 0 | 20-Oct-14 A | 04-Dec-14 A | |
| L1B-8102d | GWB Hang (Walls) & Inspection - Main Ballroom East | 1 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| SW-2114 | Zone 1 - FRP curb and gutter | 2 | 0 | 20-Oct-14 A | 14-Nov-14 A | |
| RF-4044 | Ballroom Roof - Install metal coping | 3 | 0 | 20-Oct-14 A | 13-Nov-14 A | |
| L08-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 21-Oct-14 A | 23-Oct-14 A | |
| MPT-1018 | Tower - Install Roof Penthouse (Elev 36b,37,38.39) | 5 | 0 | 21-Oct-14 A | 05-Dec-14 A | |
| L11-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2208 | Zone 2 - FRP curb and gutter | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2304 | Zone 3 - FRP curb and gutter | 3 | 0 | 21-Oct-14 A | 02-Dec-14 A | |

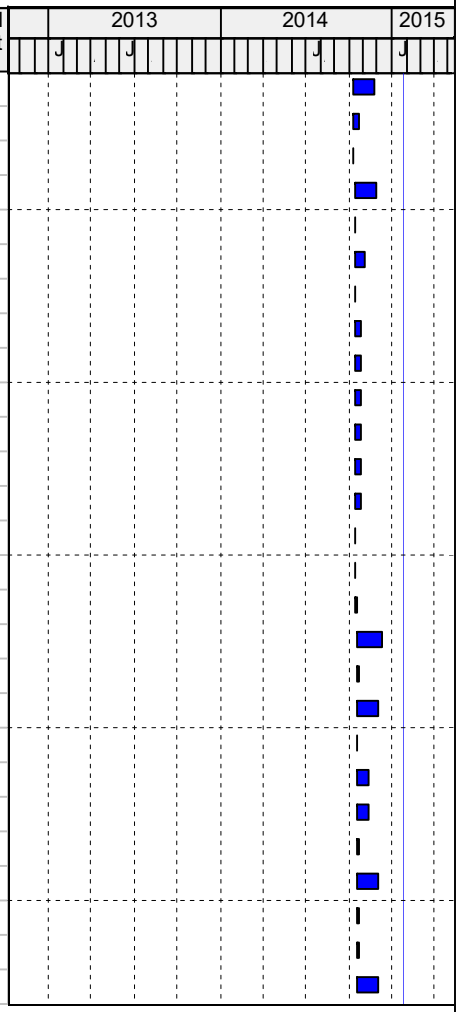



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L06-8130 | Install Door Hardware | 3 | 0 | 21-Oct-14 A | 03-Nov-14 A | |
| I-5100 | Resolve changes (ASI's and RFI's) | 1 | 0 | 21-Oct-14 A | 07-Jan-15 A | |
| L03-8634 | Pool - Install reinforcing steel & inspect | 5 | 0 | 22-Oct-14 A | 30-Oct-14 A | |
| MPT-1016 | Tower - Install N/S Wing, S. End W. of Manlift (Elev 2 | 5 | 0 | 22-Oct-14 A | 05-Dec-14 A | |
| SW-2116 | Zone 1 - Fine grade for sidewalk | 3 | 2 | 22-Oct-14 A | 09-Feb-15 | 28 |
| LL4-8106 | LL4 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| LL3-8106 | LL3 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L14-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L08-8130 | Install Door Hardware | 3 | 0 | 22-Oct-14 A | 04-Nov-14 A | |
| L07-8130 | Install Door Hardware | 3 | 0 | 22-Oct-14 A | 03-Nov-14 A | |
| L03-8606 | L3 Pool - HVAC R/I | 3 | 0 | 23-Oct-14 A | 27-Oct-14 A | |
| L09-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 23-Oct-14 A | 03-Nov-14 A | |
| L12-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| LL2-2078 | Generator - Install fuel fill control wiring | 2 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| RF-4050 | Roof at Manlift - Erect steel | 1 | 0 | 24-Oct-14 A | 24-Oct-14 A | |
| CO-7204 | Cx - Gas Service established | 0 | 0 | | 24-Oct-14 A | |
| I-5900 | Owner select color for Porte Cochere drive concrete | 20 | 15 | 24-Oct-14 A | 13-Feb-15 | 31 |
| L1BOH2-8102 | GWB Hang (Walls) | 4 | 0 | 27-Oct-14 A | 07-Nov-14 A | |
| L04-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 27-Oct-14 A | 12-Nov-14 A | |
| RF-4052 | Roof at Manlift - Framing/sheathing/air barrier (inspec | 4 | 0 | 27-Oct-14 A | 30-Oct-14 A | |
| LL2-2080 | Generator - Complete generator accessories (battery) | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| LL2-2082 | Generator - Cx fuel fill | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| L09-8130 | Install Door Hardware | 3 | 0 | 28-Oct-14 A | 04-Nov-14 A | |
| CO-7158 | Generator - Interim electrical inspection | 1 | 0 | 29-Oct-14 A | 29-Oct-14 A | |
| LL2-2070 | LL2 - Generator Room - Generator Ready for Startup | 0 | 0 | | 30-Oct-14 A | |
| LL2-2084 | Generator - Initial fuel fill | 1 | 0 | 30-Oct-14 A | 30-Oct-14 A | |

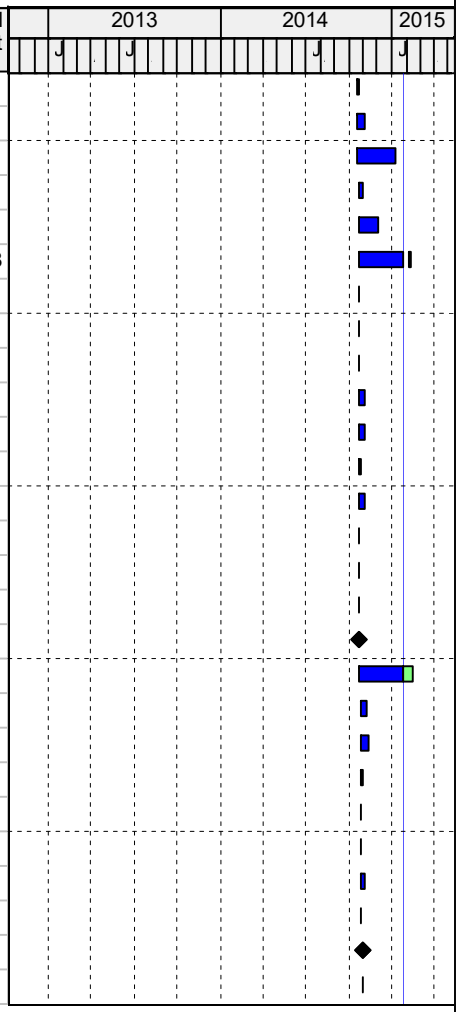


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7200 | Cx - Penthouse Mechanical Installation Complete | 0 | 0 | | 30-Oct-14 A | |
| EL-6028 | Elev 6 - RFI-761: Response, pricing, complete work (r | 20 | 2 | 30-Oct-14 A | 27-Jan-15 | 39 |
| L03-8636 | Pool - Shotcrete | 1 | 0 | 31-Oct-14 A | 31-Oct-14 A | |
| RF-4054 | Roof at Manlift - Final mechanical installations | 4 | 0 | 31-Oct-14 A | 05-Nov-14 A | |
| RF-4056 | Roof at Manlift - Final electrical connections | 2 | 0 | 31-Oct-14 A | 05-Nov-14 A | |
| CO-7130 | Fire Alarm - Point-To-Point Wiring | 18 | 2 | 01-Nov-14 A | 27-Jan-15 | 28 |
| L03-8404 | GWB Hang/Tape Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 14-Nov-14 A | |
| L04-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 14-Nov-14 A | |
| L05-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 17-Nov-14 A | |
| L06-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 17-Nov-14 A | |
| L03-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L04-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L05-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L06-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L07-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L08-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L09-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L10-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L11-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L12-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L14-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L15-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L16-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L17-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L14-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 03-Nov-14 A | 06-Nov-14 A | |
| MPT-1024 | (A) Caulking - Elevation 41 (east elevation above poo | 7 | 0 | 03-Nov-14 A | 16-Dec-14 A | |
| CO-7206 | Cx - Purge/Prove Gas-Fed Equipment and Feeder Li | 7 | 0 | 03-Nov-14 A | 09-Nov-14 A | |

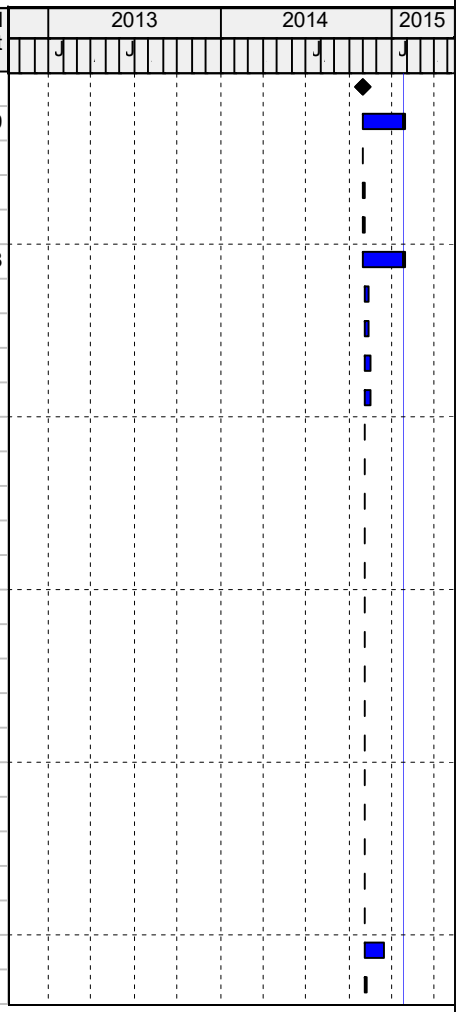



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 17-Nov-14 A | |
| L08-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L09-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L10-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L12-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L11-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 04-Nov-14 A | 15-Dec-14 A | |
| L11-8130 | Install Door Hardware | 3 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L10-8130 | Install Door Hardware | 3 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L11-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 18-Nov-14 A | |
| L12-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 19-Nov-14 A | |
| L14-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 19-Nov-14 A | |
| MPP-1010 | Podium - Install East Elevation (Elev 5 & 7) | 7 | 0 | 05-Nov-14 A | 10-Dec-14 A | |
| CO-7162 | Generator - Load bank testing | 1 | 0 | 05-Nov-14 A | 05-Nov-14 A | |
| CO-7202 | Cx - Electrical Internal Bus & LL2-L17 Bus Duct Energ | 0 | 0 | | 05-Nov-14 A | |
| CO-7202a | Cx - Energize normal power distribution | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| L15-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 19-Nov-14 A | |
| L16-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 20-Nov-14 A | |
| L17-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 20-Nov-14 A | |
| RF-4058 | Roof at Manlift - Install roofing | 2 | 0 | 06-Nov-14 A | 07-Nov-14 A | |
| CO-7164 | Generator - Final electrical inspection | 1 | 0 | 06-Nov-14 A | 06-Nov-14 A | |
| L15-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 07-Nov-14 A | 12-Nov-14 A | |
| L03-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L03-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L04-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L04-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L05-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L05-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |

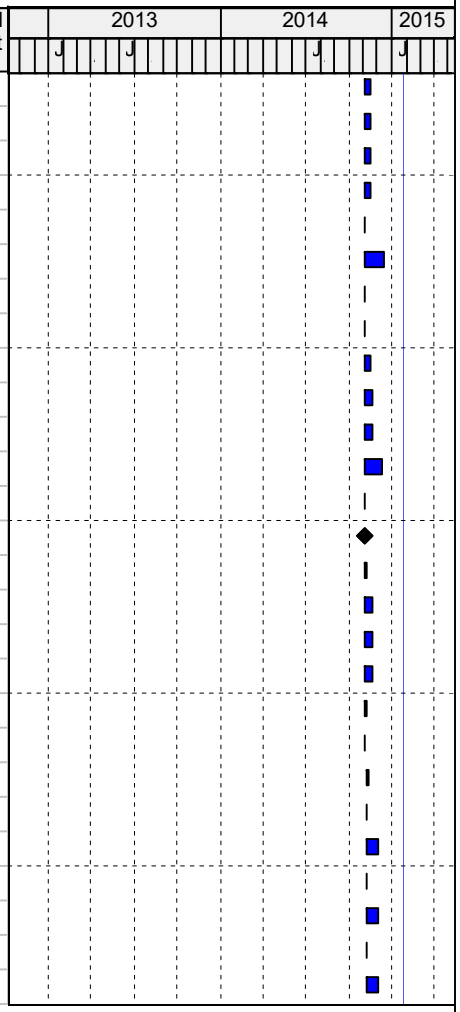



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L06-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L07-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L07-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L08-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L08-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L09-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L09-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L10-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L10-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L11-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L11-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L12-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L12-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L14-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L14-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L15-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L15-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L16-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L16-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L17-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L17-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L05-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| L06-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 10-Nov-14 A | 11-Nov-14 A | |
| MPT-1032 | Tower - Install sign backing NW (Elev 51,52) | 4 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L12-8130 | Install Door Hardware | 3 | 0 | 10-Nov-14 A | 12-Nov-14 A | |
| EL-1230 | Elev 1&2 - Complete hoistway ventilation | 13 | 0 | 10-Nov-14 A | 15-Dec-14 A | |

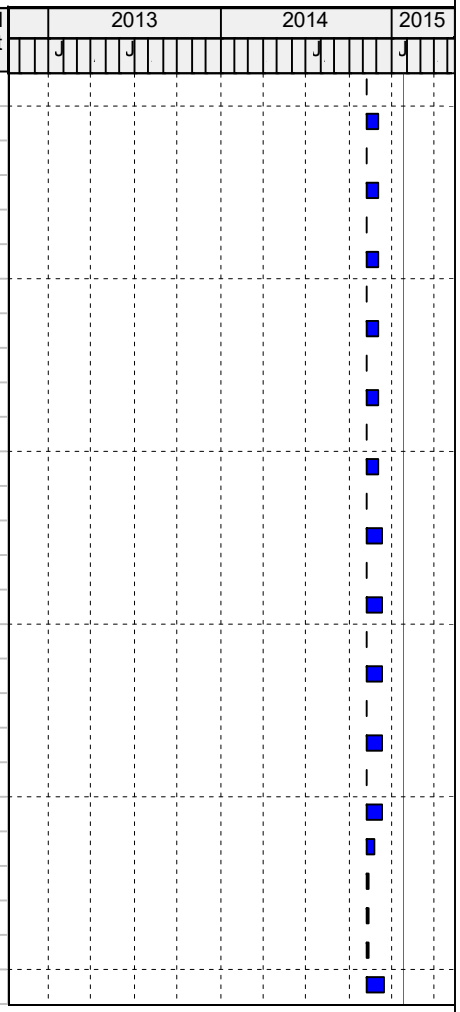



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-1232 | Elev 1&2 - Wire & startup AC split units | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-1234 | Elev 1&2 - Install EMR doors, hardware & labeling | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-3428 | Elev 3&4 - Complete hoistway ventilation | 13 | 0 | 10-Nov-14 A | 15-Dec-14 A | |
| EL-3430 | Elev 3&4 - Wire & startup AC split units | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-3432 | Elev 3&4 - Install EMR doors, hardware & labeling | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-6030 | Elev 6 - Complete fire-rated assemblies at hoistway, l | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| L07-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 11-Nov-14 A | 12-Nov-14 A | |
| L16-8106 | Paint - Accent Walls | 2 | 0 | 11-Nov-14 A | 12-Nov-14 A | |
| L14-8130 | Install Door Hardware | 3 | 0 | 11-Nov-14 A | 13-Nov-14 A | |
| L03-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 12-Nov-14 A | 18-Nov-14 A | |
| SW-2104 | Zone 1 - Install lighting conduit at SE corner | 2 | 0 | 12-Nov-14 A | 14-Nov-14 A | |
| L16-8111 | Paint - Door Jambs | 2 | 0 | 12-Nov-14 A | 13-Nov-14 A | |
| EL-6010i | Elev 6 - Pit Slab Correction (form/pour/strip/clean) | 10 | 0 | 12-Nov-14 A | 26-Nov-14 A | |
| SW-2024 | Zone 4 - FRP Porte Cochere planter & bench | 6 | 0 | 12-Nov-14 A | 04-Dec-14 A | |
| L08-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| SW-2109 | Zone 1 - Install irrigation sleeves | 2 | 0 | 13-Nov-14 A | 14-Nov-14 A | |
| MPT-1026 | (C) Caulking - Elevation 47 (north elevation, east half | 10 | 0 | 13-Nov-14 A | 19-Dec-14 A | |
| L16-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| L15-8130 | Install Door Hardware | 3 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| L04-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 14-Nov-14 A | 19-Nov-14 A | |
| SW-2203 | Zone 2 - Install irrigation sleeves | 2 | 0 | 14-Nov-14 A | 08-Jan-15 A | |
| L1B-8120 | Install operable partitions | 3 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| LL1-Z3-8340 | Install walk-in cooler/freezer (BY OTHERS) | 5 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| SW-2316 | Zone 3 - Demolish manlift shack and base | 5 | 0 | 17-Nov-14 A | 20-Nov-14 A | |
| I-1610 | Enclosure at manlift - Install exterior wall panels & ins | 5 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| L04-8140 | Install window sills | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| L03-8140x | Install window sills | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |

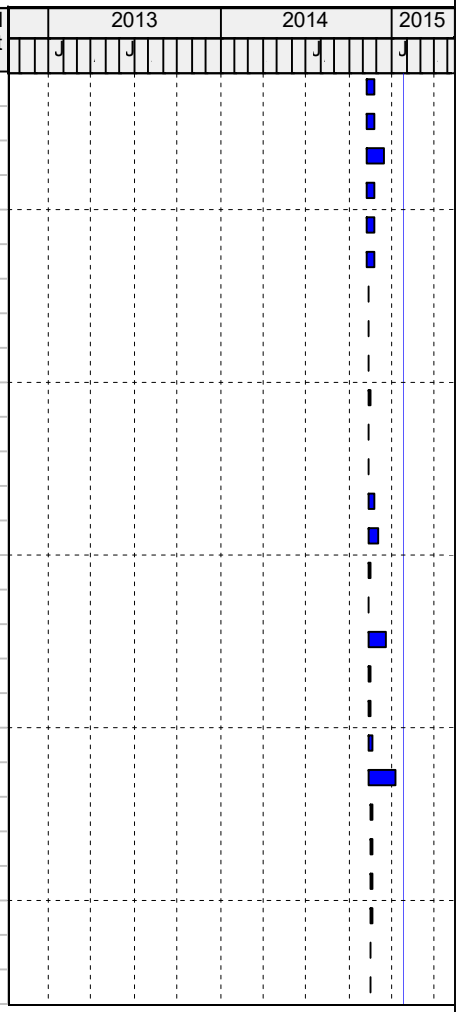



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| SW-2014 | Porte Cochere - Electrical rough-in | 5 | 0 | 17-Nov-14 A | 08-Dec-14 A | |
| I-5600 | Lower heat pump and install access panels (RFI 734) | 13 | 0 | 17-Nov-14 A | 09-Jan-15 A | |
| LL1-Z3-FCC26 | Program FACP & Stand-Up System | 20 | 5 | 17-Nov-14 A | 30-Jan-15 | 26 |
| L06-8140 | Install window sills | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L05-8140 | Install window sills | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L05-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 19-Nov-14 A | 22-Dec-14 A | |
| L16-8130 | Install Door Hardware | 3 | 0 | 19-Nov-14 A | 02-Dec-14 A | |
| L08-8140 | Install window sills | 2 | 0 | 19-Nov-14 A | 19-Nov-14 A | |
| L07-8140 | Install window sills | 2 | 0 | 19-Nov-14 A | 19-Nov-14 A | |
| I-1616 | Enclosure at manlift - Patch/repair concrete shear wal | 3 | 0 | 19-Nov-14 A | 21-Nov-14 A | |
| L10-8140 | Install window sills | 2 | 0 | 20-Nov-14 A | 20-Nov-14 A | |
| L09-8140 | Install window sills | 2 | 0 | 20-Nov-14 A | 20-Nov-14 A | |
| I-1622 | Manlift finishes - Install windows & caulk | 4 | 0 | 20-Nov-14 A | 03-Dec-14 A | |
| LL2-2060 | LL2 - Paint Laundry Room | 3 | 0 | 21-Nov-14 A | 24-Nov-14 A | |
| L03-8616 | L3 Pool - GWB above ceiling | 2 | 0 | 21-Nov-14 A | 22-Nov-14 A | |
| LL1-Z3-8342 | Final connections at walk-in cooler/freezer | 2 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L1K-8340 | Install walk-in cooler/freezer (BY OTHERS) | 2 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L10-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| L16-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| SW-2110 | Zone 1 - Adjust utilities structures | 5 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| SW-2214 | Zone 2 - Adjust utilities structures | 2 | 0 | 24-Nov-14 A | 25-Nov-14 A | |
| MPT-1030 | Tower - Install sign backing NE (Elev 44) | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| SW-2012 | Porte Cochere - Install cornice[DELETED SEE REV M | 8 | 0 | 24-Nov-14 A | 05-Dec-14 A | |
| L03-8650 | L3 Pool - Build scaffold at pool pit | 2 | 0 | 24-Nov-14 A | 25-Nov-14 A | |
| EL-6032 | Elev 6 - Install pit ladder | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| EL-6034 | Elev 6 - Install pit jack & hoistway pistons; connect hy | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |

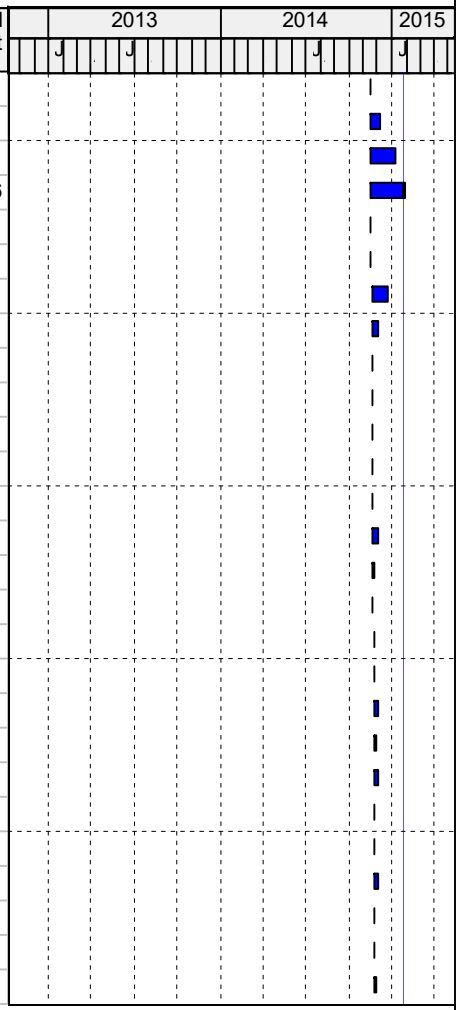



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 25-Nov-14 A | 22-Dec-14 A | |
| L02-8104a | L2 - Int Painting - South Half | 2 | 0 | 25-Nov-14 A | 26-Nov-14 A | |
| SW-2016 | Porte Cochere - Complete framing | 3 | 0 | 25-Nov-14 A | 01-Dec-14 A | |
| LL2-2096 | LL2 - Install FRP at Laundry Room | 8 | 0 | 25-Nov-14 A | 05-Dec-14 A | |
| I-1602 | Enclosure at manlift - Install shear wall clips and inspe | 4 | 0 | 26-Nov-14 A | 05-Dec-14 A | |
| L07-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| SW-2318 | Zone 3 - Install catch basin | 1 | 0 | 26-Nov-14 A | 26-Nov-14 A | |
| L03-8652 | L3 Pool - Frame ceiling | 4 | 0 | 26-Nov-14 A | 04-Dec-14 A | |
| L03-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L04-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L05-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L06-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L07-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L09-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L10-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L11-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L12-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L14-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L15-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L16-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L17-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 01-Dec-14 A | 04-Dec-14 A | |
| L02-6016a | L2 - Electrical Room Buildout | 5 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| L03-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L04-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L05-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |

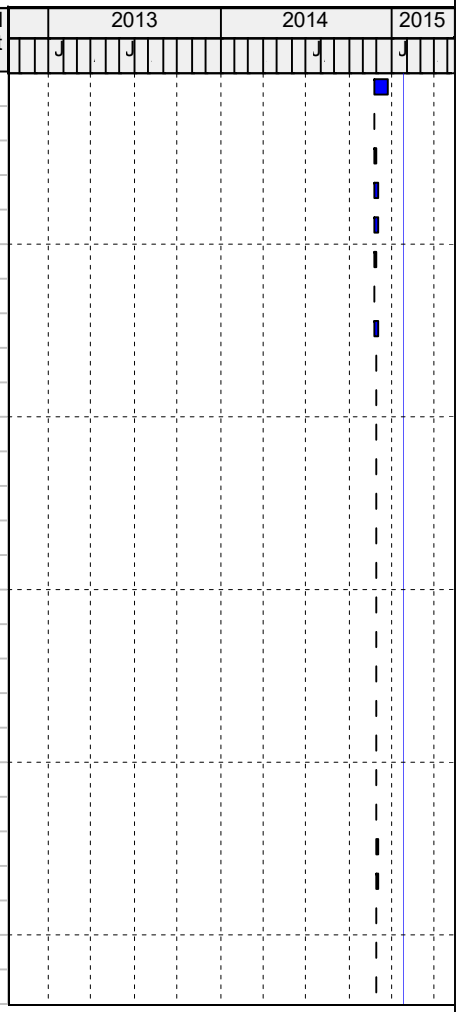



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L07-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L09-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L10-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L11-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L12-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L14-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L15-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L16-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L17-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| SW-2210 | Zone 2 - Fine grade for sidewalk | 5 | 0 | 01-Dec-14 A | 08-Jan-15 A | |
| RF-4040 | L2.5 Horseshoe - Install sheet metal capping[DELETI | 3 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| MPT-1042 | Enclosure at manlift - air barrier & inspect | 5 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| CO-7208 | Cx - Start-Up Pumps | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| CO-7210 | Cx - Start-Up VFD's | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| L17-8106 | Paint - Accent Walls | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| LL4-8116 | LL4 - Install ACT grid [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL3-8116 | LL3 - Install ACT grid [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| I-1630 | Manlift finishes - Framing, corridor ceilings & inspect | 4 | 0 | 01-Dec-14 A | 09-Dec-14 A | |
| EL-6036 | Elev 6 - Install shunt trip breaker | 5 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| L17-8111 | Paint - Door Jambs | 2 | 0 | 02-Dec-14 A | 03-Dec-14 A | |
| SW-2018 | Porte Cochere - GWB hang/tape | 3 | 0 | 02-Dec-14 A | 09-Dec-14 A | |
| L03-8654 | L3 Pool - HVAC drops at ceiling & inspect | 3 | 0 | 02-Dec-14 A | 05-Dec-14 A | |
| L11-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 03-Dec-14 A | 08-Dec-14 A | |
| SW-2308 | Zone 3 - Install site lighting | 5 | 0 | 03-Dec-14 A | 04-Dec-14 A | |
| L10-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 03-Dec-14 A | 15-Dec-14 A | |

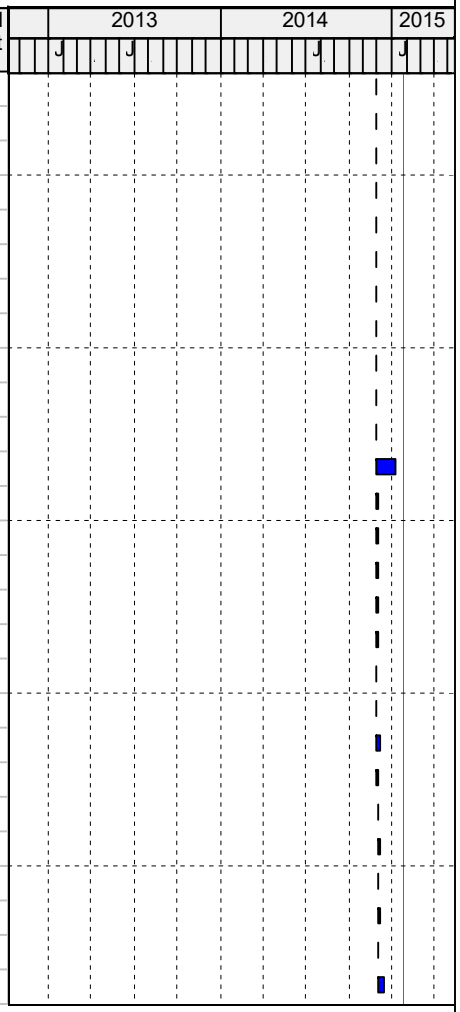



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1632 | Manlift finishes - Electrical rough-in & inspect | 2 | 0 | 03-Dec-14 A | 10-Dec-14 A | |
| SW-2028 | Zone 4 - Scan Porte Cochere deck | 2 | 0 | 04-Dec-14 A | 05-Dec-14 A | |
| I-1624 | Manlift finishes - Install batt insulation & inspect | 2 | 0 | 04-Dec-14 A | 04-Dec-14 A | |
| I-1626 | Manlift finishes - Shim window openings | 2 | 0 | 04-Dec-14 A | 05-Dec-14 A | |
| I-1628 | Manlift finishes - Install vapor barrier & inspect | 2 | 0 | 04-Dec-14 A | 08-Dec-14 A | |
| I-1608 | Tower - Install N/S Wing, S. End at manlift (Elev 32) [I | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1012 | Tower - Install N/S Wing, S. End E. Side Concrete (El | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| PC-4012 | Porte Cochere - Install sheet metal capping[DELETEI | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4046 | Tower Roof - Install sheet metal capping[DELETED S | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4060 | Roof at Manlift - Install corrugated metal panels[DELE | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4062 | Roof at Manlift - Install sheet metal capping[DELETEI | 2 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4064 | Pool Green Roof - Install sheet metal capping[DELET | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1040 | Tower - Install N/S Wing, S, End (Elev 30)[DELETED : | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1044 | Enclosure at manlift - Install sign backing south[DELE | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1612 | Enclosure at manlift - Caulking[DELETED SEE REV M | 8 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1614 | Enclosure at manlift - Install rigid insulation at shear w | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1618 | Enclosure at manlift - Install framing at shear wall[DEI | 5 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1620 | Enclosure at manlift - Install hat channel over framing | 5 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| L03-8656 | L3 Pool - Electrical rough-in at ceiling & inspect | 3 | 0 | 05-Dec-14 A | 19-Dec-14 A | |
| L1K-8344 | Set kitchen hoods | 8 | 0 | 06-Dec-14 A | 15-Dec-14 A | |
| L12-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L03-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |
| L04-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |
| L05-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |
| SW-2312 | Zone 3 - Fine grade for sidewalk | 3 | 0 | 08-Dec-14 A | 08-Jan-15 A | |
| RF-4042 | Pool Roof - Install metal coping at high roof | 2 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L17-8130 | Install Door Hardware | 3 | 0 | 08-Dec-14 A | 11-Dec-14 A | |

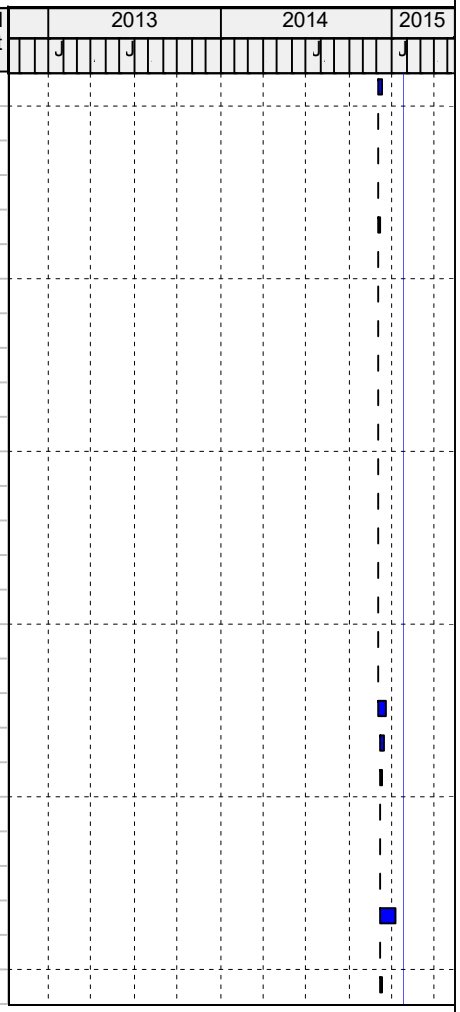



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L03-8658 | L3 Pool - Fire sprinkler drops at ceiling & inspect | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| LL2-8140 | LL2 - Install vinyl wall coverings | 2 | 0 | 08-Dec-14 A | 24-Dec-14 A | |
| L04-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L05-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L07-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L08-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L14-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L15-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 09-Dec-14 A | 12-Dec-14 A | |
| L03-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L07-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L08-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L04-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L05-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L07-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L08-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| RF-4072 | Pool Roof - Install metal coping | 3 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L17-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 09-Dec-14 A | 12-Dec-14 A | |
| L07-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 09-Dec-14 A | 29-Dec-14 A | |

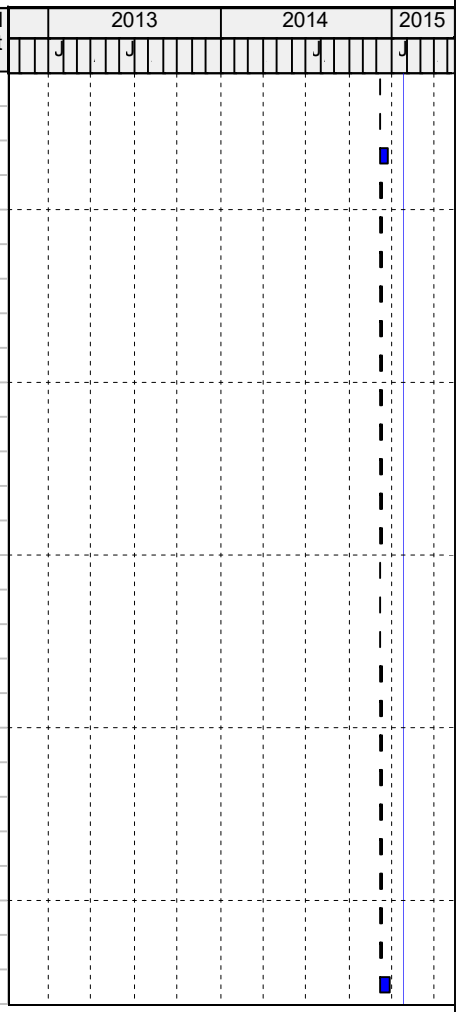



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 09-Dec-14 A | 24-Dec-14 A | |
| I-1604 | Manlift finishes - GWB, hang walls | 2 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L07-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L08-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 16-Dec-14 A | |
| L11-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L12-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L14-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L15-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L16-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L17-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| LL2E-8340 | LL2 - Install walk-in cooler/freezer (BY OTHERS) | 5 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L10-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 10-Dec-14 A | 17-Dec-14 A | |
| L09-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L10-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L11-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L11-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L12-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L14-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L15-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L16-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L17-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L08-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 10-Dec-14 A | 29-Dec-14 A | |
| I-1634 | Manlift finishes - GWB, hang ceilings | 2 | 0 | 10-Dec-14 A | 16-Dec-14 A | |
| L12-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L14-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L15-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L03-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 11-Dec-14 A | 11-Dec-14 A | |

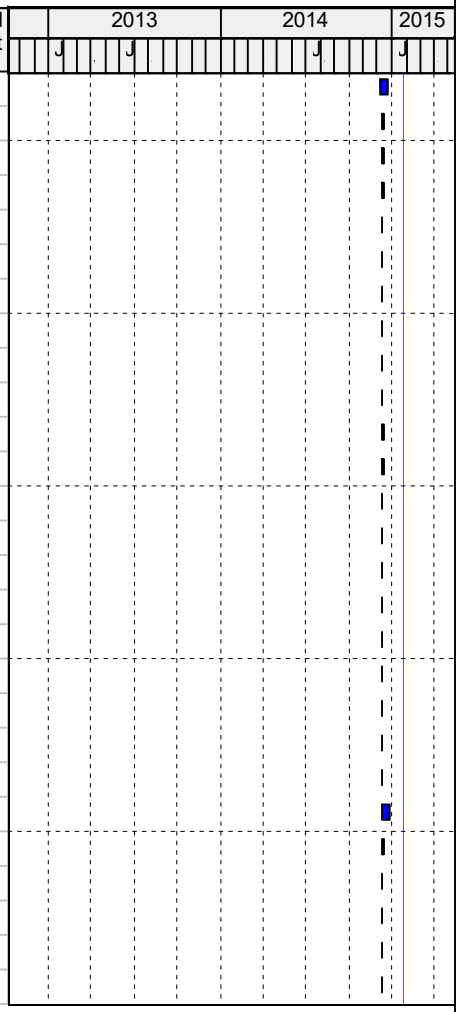



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| MPT-1034 | (A) Elevation 52 (west elevation, north end, L3-L18) | 4 | 0 | 11-Dec-14 A | 16-Dec-14 A | |
| MPT-1036 | (B) Elevation 45/46 (north elevation, east end, L3-L1 | 5 | 0 | 11-Dec-14 A | 19-Dec-14 A | |
| L16-7030 | Paint | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L17-7030 | Paint | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L05-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L06-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| MPT-1066 | Tower Sign, East (El. 32) - Install backing | 3 | 0 | 12-Dec-14 A | 22-Dec-14 A | |
| MPT-1076 | (B) Caulking - Elevation 51 (north elevation, west half | 10 | 0 | 12-Dec-14 A | 19-Dec-14 A | |
| L04-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L04-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L07-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L08-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L09-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L14-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L15-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L17-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 16-Dec-14 A | |
| L04-7042 | Install Tile Flooring (x41) | 2 | 0 | 15-Dec-14 A | 24-Dec-14 A | |
| L05-7042 | Install Tile Flooring (x41) | 2 | 0 | 15-Dec-14 A | 24-Dec-14 A | |
| LL4-8102a | LL4 - GWB Tape/Finish | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| LL3-8102a | LL3 - GWB Tape/Finish | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| L03-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L04-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |

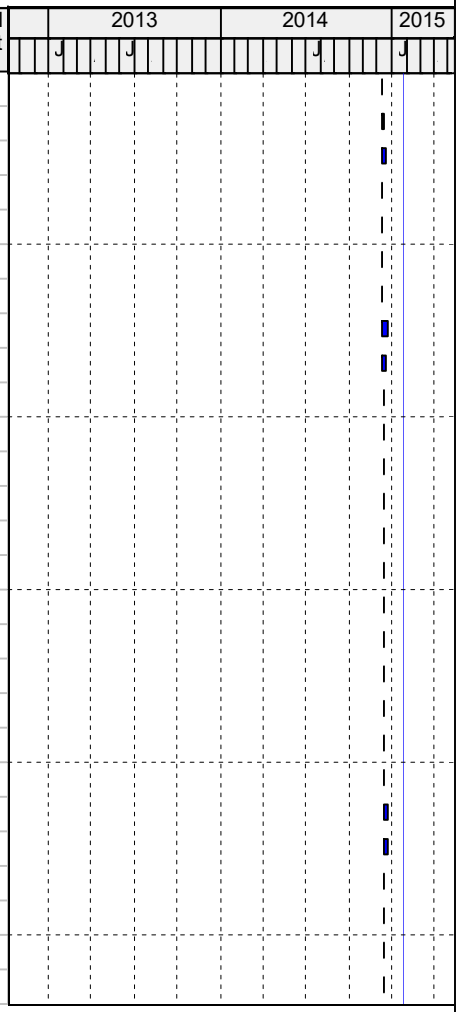



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L07-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L08-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L09-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L10-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| CO-7126 | Fire pump test pre-planning complete (see checklist) | 0 | 0 | | 15-Dec-14 A | |
| LL1-Z3-6034 | COB Correction - Add ceiling access panels in Food F | 10 | 1 | 15-Dec-14 A | 26-Jan-15 | 19 |
| I-5200 | Receive ceiling grid layout from owner and adjust ME | 8 | 5 | 15-Dec-14 A | 30-Jan-15 | 21 |
| L03-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| L05-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L09-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L10-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L10-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L11-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L11-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L14-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L15-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L16-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L17-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| LL2E-8342 | LL2 - Final connections at walk-in cooler/freezer | 5 | 0 | 16-Dec-14 A | 05-Jan-15 A | |
| L11-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 16-Dec-14 A | 18-Dec-14 A | |
| L16-8201 | Corridors - Install ACT Grid | 2 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L06-7042 | Install Tile Flooring (x41) | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L07-7042 | Install Tile Flooring (x41) | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |

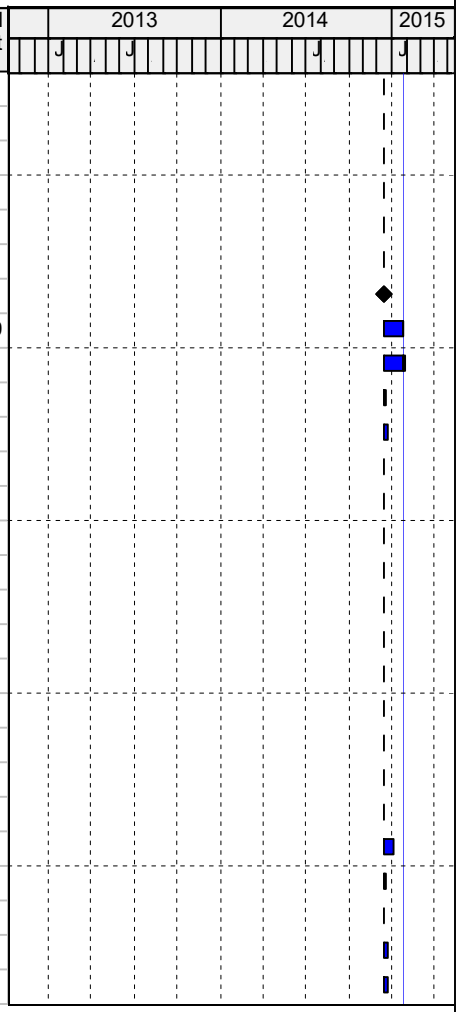



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-8102a | GWB Hang (Ceilings) & Inspection | 3 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L11-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L14-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L15-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L16-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L17-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| CO-7128 | Run fire pump test | 2 | 0 | 16-Dec-14 A | 17-Dec-14 A | |
| L09-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 16-Dec-14 A | 30-Dec-14 A | |
| SW-2026 | Zone 4 - FRP NW planter | 5 | 0 | 16-Dec-14 A | 05-Jan-15 A | |
| I-5370 | (S) Resolve south tower sign backing (RFI 844) | 5 | 0 | 16-Dec-14 A | 09-Jan-15 A | |
| L03-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 22-Dec-14 A | |
| L04-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 23-Dec-14 A | |
| L06-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 29-Dec-14 A | |
| L07-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 30-Dec-14 A | |
| L08-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 31-Dec-14 A | |
| L09-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 05-Jan-15 A | |
| L14-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L15-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L16-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L17-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L08-7042 | Install Tile Flooring (x41) | 2 | 0 | 17-Dec-14 A | 24-Dec-14 A | |
| L09-7042 | Install Tile Flooring (x41) | 2 | 0 | 17-Dec-14 A | 24-Dec-14 A | |
| L04-7136 | Install Door and Hardware | 1 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L16-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 17-Dec-14 A | 29-Dec-14 A | |
| MPT-1046 | (A) Elevation 26/27/53 (west elevation, south of 52, L | 3 | 0 | 17-Dec-14 A | 18-Dec-14 A | |
| MPT-1057 | (S) Elevation 32 framing (south elevation, east of mai | 5 | 0 | 17-Dec-14 A | 19-Jan-15 A | |

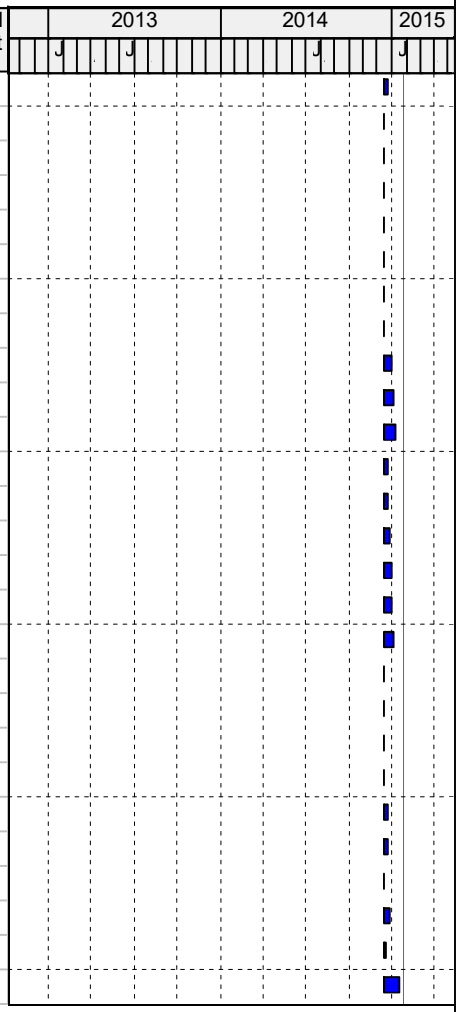



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPT-1080 | (A) Caulking - Elevation 44 (east elevation above poo | 8 | 0 | 17-Dec-14 A | 22-Dec-14 A | |
| LL1-Z2-8108 | Framing, ceiling clouds (incl. inspection) | 5 | 0 | 17-Dec-14 A | 22-Jan-15 A | |
| MPP-1006 | (C) Install Level 3 cornice metal (north, west & south) | 6 | 2 | 18-Dec-14 A | 27-Jan-15 | 16 |
| L10-7042 | Install Tile Flooring (x41) | 2 | 0 | 18-Dec-14 A | 24-Dec-14 A | |
| L11-7042 | Install Tile Flooring (x41) | 2 | 0 | 18-Dec-14 A | 24-Dec-14 A | |
| L12-7042 | Install Tile Flooring (x41) | 2 | 0 | 19-Dec-14 A | 24-Dec-14 A | |
| L14-7042 | Install Tile Flooring (x41) | 2 | 0 | 19-Dec-14 A | 24-Dec-14 A | |
| MPT-1048 | (B) Elevation 37 (penthouse east) | 3 | 0 | 19-Dec-14 A | 20-Dec-14 A | |
| I-5000 | Resolve RFI's and site work changes (new drawings) | 10 | 0 | 19-Dec-14 A | 14-Jan-15 A | |
| I-5002 | Resolve RFI's and site work changes (new drawings) | 20 | 10 | 19-Dec-14 A | 06-Feb-15 | 17 |
| I-5003 | Resolve RFI's and site work changes (new drawings) | 10 | 0 | 19-Dec-14 A | 16-Jan-15 A | |
| I-5004 | Resolve RFI's and site work changes (new drawings) | 1 | 0 | 19-Dec-14 A | 16-Jan-15 A | |
| L03-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 22-Dec-14 A | 22-Dec-14 A | |
| L07-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L17-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| CO-7212 | Cx - Start-Up Boilers | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L17-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L08-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L07-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L06-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L05-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L04-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 22-Dec-14 A | |
| I-1636 | Manlift finishes - GWB, tape & finish | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| EL-6038 | Elev 6 - Rough-in call boxes & lanterns | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| EL-6052 | Elev 6 - Complete hoistway ventilation | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| MPT-1078 | (C) Caulking - Elevation 37/38/39 (penthouse) | 4 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| MPT-1086 | (A) Caulking - Elevation 45/46 (north elevation, east e | 7 | 0 | 22-Dec-14 A | 29-Dec-14 A | |

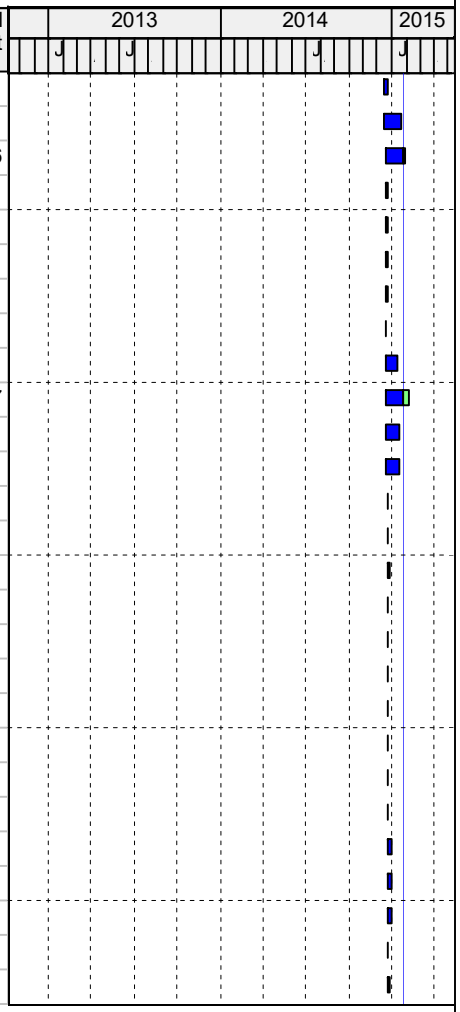


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPT-1088 | (B) Caulking - Elevation 52/53/26/27 (west elevation, | 11 | 0 | 22-Dec-14 A | 02-Jan-15 A | |
| MPP-1044 | Caulking - Elevation 9/10/11/12/13 (upper ballroom) | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| MPP-1046 | Caulking - Elevation 5/6 (east elevation, south end) | 8 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| L03-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L03-7032 | Install VCT Flooring (x42) | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L08-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L10-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L09-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L09-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 24-Dec-14 A | 29-Dec-14 A | |
| L03-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 31-Dec-14 A | |
| L15-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L16-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L17-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L04-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L05-7136 | Install Door and Hardware | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L10-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L17-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| LL1-Z3-8202 | Install FRP wall coverings | 4 | 0 | 29-Dec-14 A | 06-Jan-15 A | |
| L04-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L05-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L06-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L07-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L08-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L09-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L10-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL2-8130 | LL2 - Install ceiling grid | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| I-5300 | Heat Pump Revision - demo existing ceiling framing | 2 | 0 | 29-Dec-14 A | 29-Dec-14 A | |

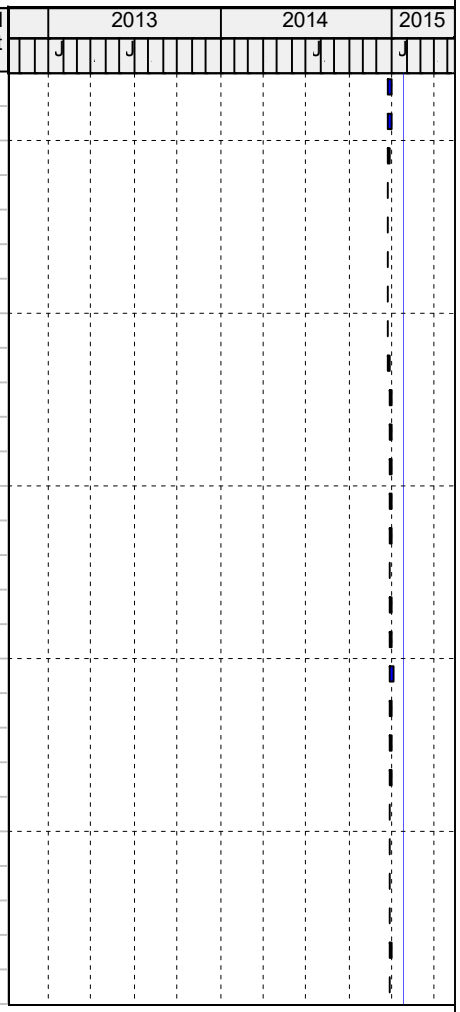



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 30-Dec-14 A | 05-Jan-15 A | |
| L06-7136 | Install Door and Hardware | 1 | 0 | 30-Dec-14 A | 30-Dec-14 A | |
| L11-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 30-Dec-14 A | 31-Dec-14 A | |
| I-5302 | Heat Pump Revision - rework MEP at celing | 5 | 0 | 30-Dec-14 A | 12-Jan-15 A | |
| I-1606 | Manlift finishes - Prime & paint | 4 | 0 | 31-Dec-14 A | 06-Jan-15 A | |
| L07-7136 | Install Door and Hardware | 1 | 0 | 31-Dec-14 A | 31-Dec-14 A | |
| L12-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 31-Dec-14 A | 05-Jan-15 A | |
| CO-7214 | Cx - Flush & Fill HVAC Hydronics Systems | 5 | 0 | 02-Jan-15 A | 05-Jan-15 A | |
| MPP-1032 | (C) Elevation 23/24/25 (Porte Cochere north, below c | 5 | 0 | 02-Jan-15 A | 19-Jan-15 A | |
| L1BOH2-8215 | GWB tape & finish walls & ceilings | 7 | 7 | 05-Jan-15 A | 09-Feb-15 | 14 |
| L10-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| L11-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 13-Jan-15 A | |
| L12-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 13-Jan-15 A | |
| L14-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| L16-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L04-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L05-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L06-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L05-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| L06-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L07-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L08-7136 | Install Door and Hardware | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L08-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L09-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L10-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L14-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| SW-2314 | Zone 3 - FRP sidewalk | 5 | 2 | 05-Jan-15 A | 03-Feb-15 | 33 |

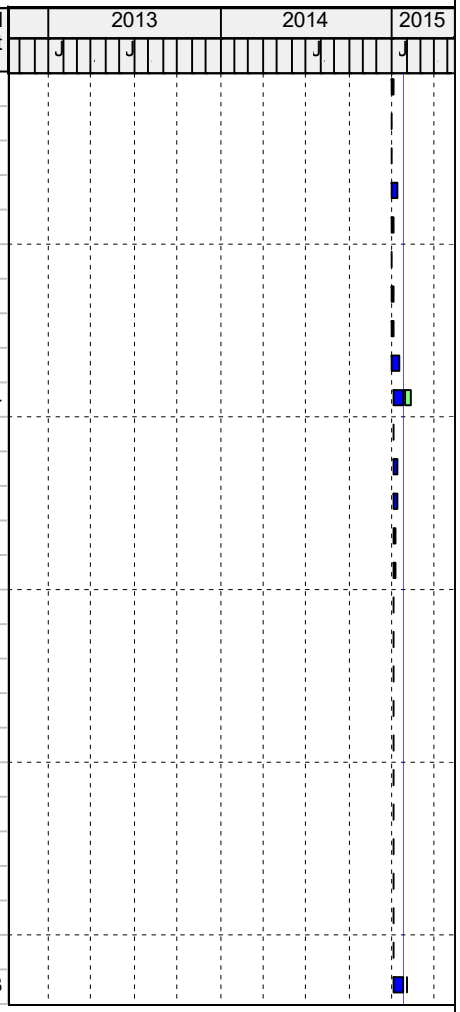



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8203 | Wall coverings - vinyl at corridors | 2 | 1 | 05-Jan-15 A | 26-Jan-15 | 26 |
| CO-7240 | Cx - Heat Pump Start-Up - Levels 3 & 4 | 5 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| SW-2220 | Zone 2 - FRP curb/gutter at NW corner | 4 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| MPT-1054 | (A) Complete Elevation 30 (south elevation, west of n | 5 | 1 | 05-Jan-15 A | 02-Feb-15 | 18 |
| MPP-1028 | (C) Tapered pilasters, west | 3 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| MPP-1030 | (C) Tapered pilasters, east | 3 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| LL2-8142 | HVAC drops/trim to grid | 3 | 0 | 05-Jan-15 A | 19-Jan-15 A | |
| L1L-8216 | Complete electrical/fire alarm drops @ ceilings | 5 | 0 | 05-Jan-15 A | 08-Jan-15 A | |
| L1BOH2-8217 | GWB hang ceilings and at heat pumps | 10 | 4 | 05-Jan-15 A | 29-Jan-15 | 14 |
| L1L-8222 | Complete HVAC drops @ ceilings | 5 | 0 | 05-Jan-15 A | 23-Jan-15 A | |
| L1L-8224 | Complete fire sprinkler drops @ ceilings | 5 | 0 | 05-Jan-15 A | 08-Jan-15 A | |
| L1L-8254 | Complete electrical rough-in at walls | 5 | 1 | 05-Jan-15 A | 26-Jan-15 | 0 |
| I-5350 | Fabricate & install new hydraulic ram | 30 | 4 | 05-Jan-15 A | 29-Jan-15 | 37 |
| SW-2226 | Zone 2 - Procure light poles and replacement luminai | 25 | 15 | 05-Jan-15 A | 13-Feb-15 | 23 |
| LL1-8120 | Complete GWB tape & finish in corridors | 7 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| L1K-8108 | Complete kitchen hood installation and fire blanket wi | 10 | 7 | 05-Jan-15 A | 03-Feb-15 | 8 |
| L1K-8110 | Complete MEP rough-in above ceiling | 10 | 2 | 05-Jan-15 A | 03-Feb-15 | 9 |
| L1B-8122 | Framing, complete ceiling at corridors | 5 | 0 | 05-Jan-15 A | 13-Jan-15 A | |
| I-5102 | Bar lighting layout - resolve conflicts (RFI) | 7 | 0 | 05-Jan-15 A | 19-Jan-15 A | |
| I-5110 | Bar radius ceiling - resolve framing issues | 5 | 0 | 05-Jan-15 A | 14-Jan-15 A | |
| I-5120 | Dining feature wall - resolve design issues | 7 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| L02-8178 | Complete heat pump enclosures | 5 | 0 | 05-Jan-15 A | 12-Jan-15 A | |
| I-5850 | Owner provide revised lighting layout | 10 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| I-5130 | Bar plumbing relocation - resolve conflicts | 25 | 9 | 05-Jan-15 A | 05-Feb-15 | 10 |
| I-5140 | Damper at BPF #8 - resolve conflicts | 30 | 10 | 05-Jan-15 A | 06-Feb-15 | 3 |
| I-5150 | Sprinkler pipe furring - resolve conflicts | 15 | 3 | 05-Jan-15 A | 28-Jan-15 | 1 |
| I-5160 | ASI 63 electrical revisions - resolve conflicts | 10 | 0 | 05-Jan-15 A | 16-Jan-15 A | |

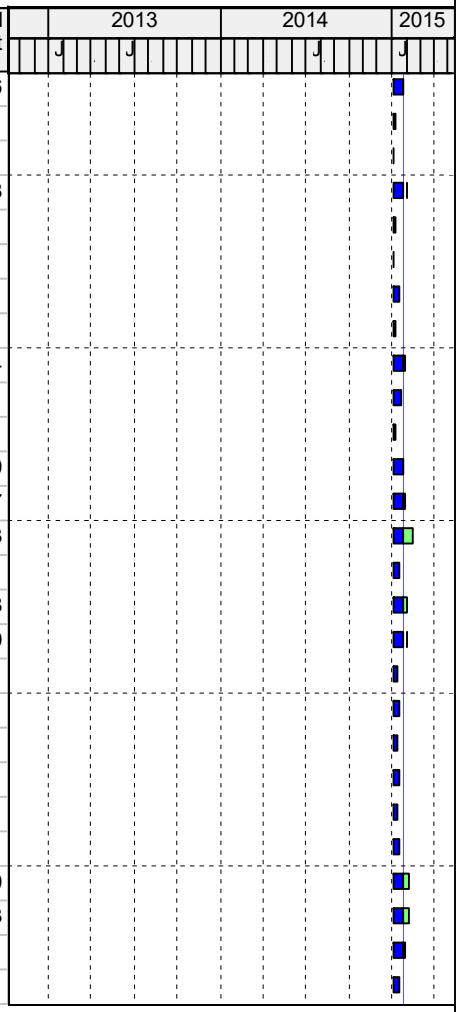



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 06-Jan-15 A | 07-Jan-15 A | |
| L07-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L08-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L09-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L10-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L09-7136 | Install Door and Hardware | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L10-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L11-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L12-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L15-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 06-Jan-15 A | 07-Jan-15 A | |
| L11-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 06-Jan-15 A | 12-Jan-15 A | |
| L03-8660 | GWB hang ceilings at Pool | 3 | 1 | 06-Jan-15 A | 26-Jan-15 | 2 |
| L1K-6011 | Complete HVAC RI @ ceilings | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L1K-6013 | Complete electrical rough-in @ ceilings & inspection | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L1K-6015 | Complete fire sprinkler RI @ ceilings | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L12-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L14-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L15-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L16-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L15-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 07-Jan-15 A | 20-Jan-15 A | |
| L12-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 07-Jan-15 A | 13-Jan-15 A | |
| CO-7242 | Cx - Heat Pump Start-Up - Levels 5 & 6 | 5 | 0 | 07-Jan-15 A | 09-Jan-15 A | |
| CO-7252 | Cx - Start-Up - FSD & SD Operation Verification | 10 | 5 | 07-Jan-15 A | 30-Jan-15 | 28 |
| MPP-1026 | (B) Complete Elevation 7/8 (east elevation) | 5 | 1 | 07-Jan-15 A | 24-Feb-15 | 24 |
| LL1-6014Ib2 | L1 bar redesign - GWB hang, tape, finish (including ir | 12 | 5 | 08-Jan-15 A | 30-Jan-15 | 18 |
| SW-2310 | Zone 3 - Install irrigation sleeves | 2 | 0 | 08-Jan-15 A | 08-Jan-15 A | |
| I-1638 | Manlift finishes - ceiling grid | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |

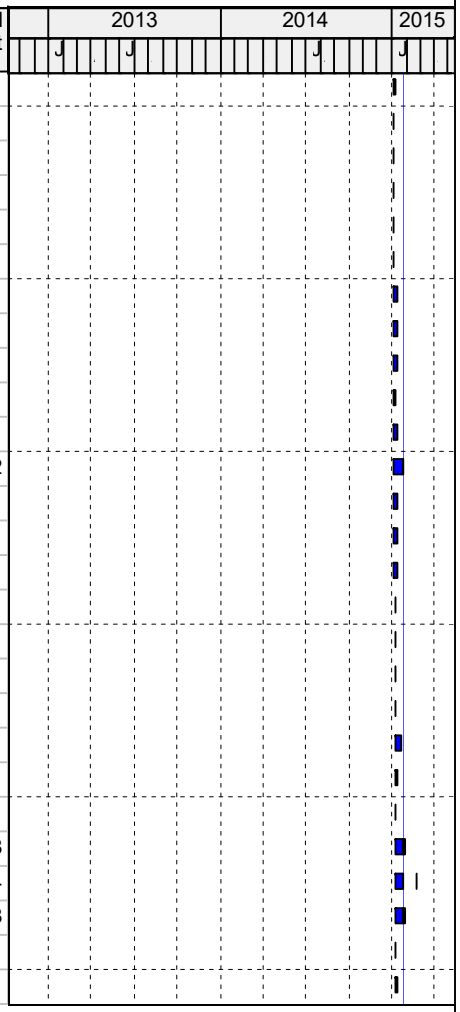


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8662 | GWB tape & finish ceilings at Pool | 7 | 7 | 08-Jan-15 A | 04-Feb-15 | 2 |
| MPT-1072 | Tower Sign, West (El, 52) | 5 | 3 | 08-Jan-15 A | 02-Feb-15 | 42 |
| L1L-8220 | Complete fire sprinkler RI @ ceilings | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| L1L-8270 | Complete HVAC RI @ ceilings | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| SW-2224 | Zone 2 - Adjust Comcast vault lids | 2 | 0 | 08-Jan-15 A | 08-Jan-15 A | |
| I-1212 | Resolve stud/duct conflict at east wall | 5 | 0 | 08-Jan-15 A | 14-Jan-15 A | |
| L04-8218 | Install base at corridors (& approve mockup) | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| GB410-100 | Complete GWB - Levels 4-10 | 5 | 0 | 08-Jan-15 A | 14-Jan-15 A | |
| LL1-6014Ib4 | L1 bar redesign - complete reframing | 5 | 0 | 08-Jan-15 A | 19-Jan-15 A | |
| I-5306 | Heat Pump Revision - complete reframing | 5 | 0 | 08-Jan-15 A | 19-Jan-15 A | |
| L15-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L16-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8121 | Install Bathroom "Barn Doors" | 3 | 1 | 12-Jan-15 A | 28-Jan-15 | 29 |
| L04-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L05-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L06-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L07-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L08-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L09-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L10-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L11-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L12-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L14-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L15-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L11-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |

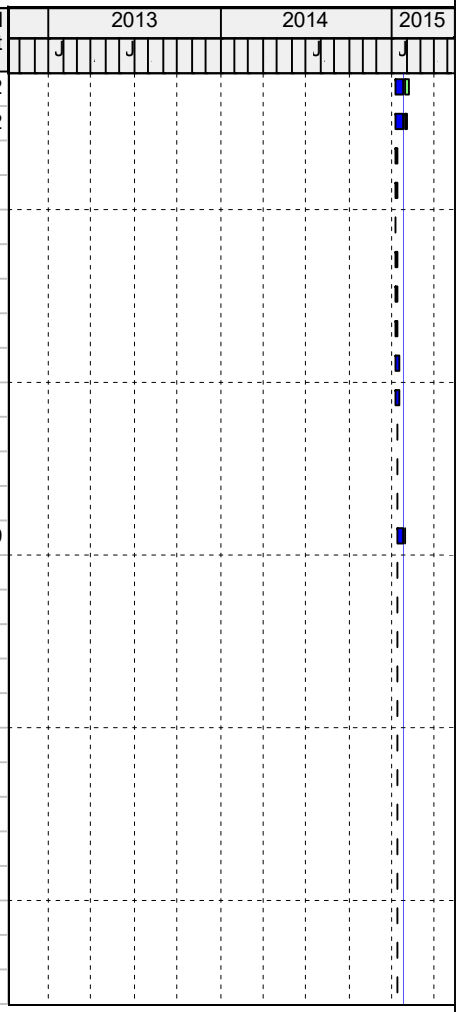



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-7136 | Install doors & hardware | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L14-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L15-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L15-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L14-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L11-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L03-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 12-Jan-15 A | 19-Jan-15 A | |
| CO-7244 | Cx - Heat Pump Start-Up - Levels 7 & 8 | 5 | 0 | 12-Jan-15 A | 14-Jan-15 A | |
| MPT-1058 | (A) Elevation 32 hat channel (south elevation, east of | 3 | 3 | 12-Jan-15 A | 31-Jan-15 | 18 |
| MPT-1068 | Tower Sign, North (El. 51) | 5 | 3 | 12-Jan-15 A | 28-Jan-15 | 42 |
| L03-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L11-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L14-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L15-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L02-8144 | GWB hang at Locker Rooms | 2 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| SW-2326 | Zone 3 - Install j-boxes | 3 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| I-5800 | Mechanical correction notice - interference with light t | 10 | 4 | 12-Jan-15 A | 29-Jan-15 | 0 |
| I-5602 | Frame FCC ceiling | 2 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| CO-7166 | Replace exhaust fitting | 10 | 3 | 12-Jan-15 A | 28-Jan-15 | 67 |
| MPP-1034 | Deliver Elevation 48 corner panels | 25 | 21 | 12-Jan-15 A | 23-Feb-15 | 31 |
| MPP-1042 | Deliver Elevation 32 corner panels | 25 | 21 | 12-Jan-15 A | 23-Feb-15 | 10 |
| MPP-1066 | Deliver Elevation 33/34 corner panels | 25 | 21 | 12-Jan-15 A | 23-Feb-15 | 16 |
| MPP-1068 | Deliver Elevation 32 spandrel panel head/sill flashings | 25 | 21 | 12-Jan-15 A | 23-Feb-15 | 17 |
| MPP-1070 | Deliver Elevation 44 spandrel panel head/sill flashings | 25 | 21 | 12-Jan-15 A | 23-Feb-15 | 17 |
| MPP-1072 | Deliver remaining Elevation 4 panels | 25 | 21 | 12-Jan-15 A | 23-Feb-15 | 29 |

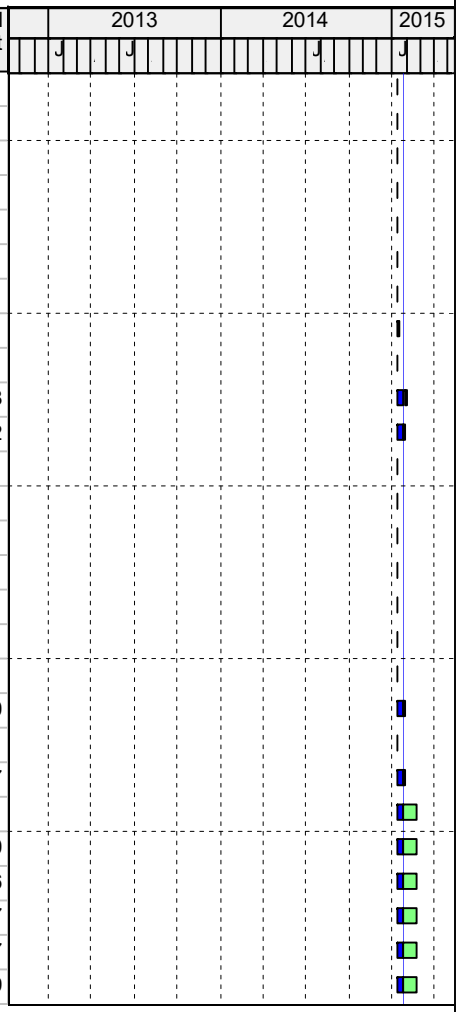



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPP-1074 | Deliver remaining Elevation 7 panels | 25 | 21 | 12-Jan-15 A | 23-Feb-15 | 20 |
| MPP-1076 | Deliver Pool cornice panels | 25 | 20 | 12-Jan-15 A | 20-Feb-15 | 10 |
| L15-7136 | Install doors & hardware | 1 | 1 | 13-Jan-15 A | 26-Jan-15 | 48 |
| L03-8664 | Paint, prime & first coat finish at Pool | 3 | 2 | 13-Jan-15 A | 06-Feb-15 | 2 |
| MPP-1022 | (A) Complete Elevation 40 (pool south elevation, L3-L | 5 | 0 | 13-Jan-15 A | 20-Jan-15 A | |
| L05-8226 | Install base at corridors | 1 | 0 | 13-Jan-15 A | 13-Jan-15 A | |
| L16-8138 | Bathrooms - Install toilet accessories | 2 | 0 | 14-Jan-15 A | 15-Jan-15 A | |
| L14-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| CO-7246 | Cx - Heat Pump Start-Up - Levels 9 & 10 | 5 | 0 | 14-Jan-15 A | 16-Jan-15 A | |
| I-5604 | GWB hang, tape & finish FCC ceiling | 5 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| L14-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 15-Jan-15 A | 16-Jan-15 A | |
| L16-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 15-Jan-15 A | 21-Jan-15 A | |
| SW-2126 | Zone 1 - Remove temporary transformer | 5 | 3 | 15-Jan-15 A | 28-Jan-15 | 28 |
| I-5112 | Bar radius ceiling - complete framing | 5 | 0 | 15-Jan-15 A | 20-Jan-15 A | |
| L07-8226 | Install base at corridors | 1 | 0 | 16-Jan-15 A | 16-Jan-15 A | |
| L16-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| CO-7248 | Cx - Heat Pump Start-Up - Levels 11 & 12 | 5 | 0 | 19-Jan-15 A | 21-Jan-15 A | |
| SW-2020 | Porte Cochere - EIFS at ceiling | 7 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L02-8146 | GWB tape & finish at Locker Rooms | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L1K-8138 | Complete GWB hang & tape | 9 | 4 | 19-Jan-15 A | 29-Jan-15 | 16 |
| L1L-8252 | Complete electrical/fire alarm rough-in @ ceilings | 3 | 1 | 19-Jan-15 A | 26-Jan-15 | 13 |
| LL1-8122 | Paint corridors | 6 | 0 | 19-Jan-15 A | 21-Jan-15 A | |
| L1B-6027 | Framing, ceiling at East Ballroom | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L09-8226 | Install base at corridors | 1 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| GB410-102 | Complete painting - Levels 4-10 | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL1-Z2-8110 | Paint, prime & first coat finish at Meeting Rooms | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| I-5122 | Dining feature wall - complete framing | 3 | 0 | 19-Jan-15 A | 21-Jan-15 A | |

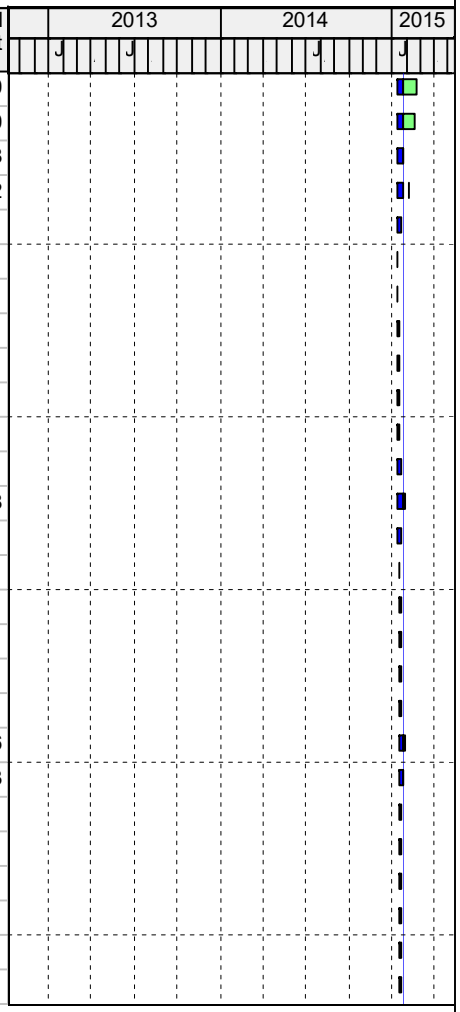



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-5162 | ASI 63 electrical revisions - demo existing | 1 | 0 | 19-Jan-15 A | 19-Jan-15 A | |
| L1B-8170 | Complete cover inspections | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L17-8138 | Bathrooms - Install toilet accessories | 2 | 1 | 20-Jan-15 A | 03-Feb-15 | 28 |
| MPP-1014 | Caulking - Elevation 1/2/A/B/C/23/24/25 (west elevati | 9 | 5 | 20-Jan-15 A | 30-Jan-15 | 53 |
| L03-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| LL1-8202 | HVAC trim at ceiling | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| LL1-8206 | Lighting & electrical trim | 4 | 1 | 20-Jan-15 A | 26-Jan-15 | 21 |
| LL1-8208 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| LL1-Z2-8138 | Paint corridors | 3 | 3 | 20-Jan-15 A | 09-Feb-15 | 22 |
| L10-8226 | Install base at corridors | 1 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| GB410-106 | Complete flooring - Levels 4-10 | 3 | 1 | 20-Jan-15 A | 26-Jan-15 | 31 |
| L04-8422 | Floor prep | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| I-5606 | Paint FCC ceiling | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| I-5104 | Bar lighting layout - complete elecrical rough-in | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| I-5164 | ASI 63 electrical revisions - revise electrical | 3 | 1 | 20-Jan-15 A | 26-Jan-15 | 1 |
| L16-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| CO-7222 | Cx - Start-Up - Kitchen Exhaust Fans | 2 | 1 | 21-Jan-15 A | 04-Feb-15 | 34 |
| L15-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L14-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L12-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L11-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L16-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| CO-7250 | Cx - Heat Pump Start-Up - Levels 14 & 15 | 5 | 0 | 21-Jan-15 A | 23-Jan-15 A | |
| L16-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| I-5304 | Heat Pump Revision - rework GWB | 9 | 5 | 21-Jan-15 A | 30-Jan-15 | 18 |
| L03-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L04-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |

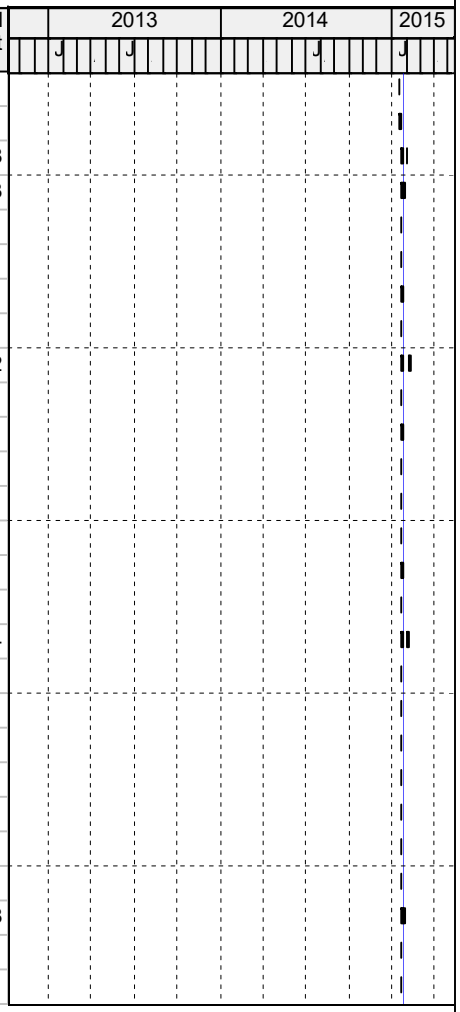



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L06-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L07-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L08-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L09-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L11-8226 | Install base at corridors | 1 | 0 | 21-Jan-15 A | 22-Jan-15 A | |
| L05-8422 | Floor prep | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L07-7134 | Flooring - VCT | 1 | 0 | 22-Jan-15 A | 22-Jan-15 A | |
| L17-8203 | Wall coverings - vinyl at corridors | 3 | 2 | 22-Jan-15 A | 29-Jan-15 | 28 |
| LL1-8210 | Fire sprinkler trim | 1 | 0 | 22-Jan-15 A | 22-Jan-15 A | |
| L12-8226 | Install base at corridors | 1 | 0 | 22-Jan-15 A | 23-Jan-15 A | |
| MPP-1016 | Caulking - Elevation 7/8 (east elevation) | 8 | 6 | 23-Jan-15 A | 04-Mar-15 | 20 |
| LL1-Z2-8120 | GWB hang, tape & finish ceiling clouds at Jr. Ballroon | 7 | 7 | 23-Jan-15 A | 03-Feb-15 | 13 |
| LL1-Z3-8148 | Paint Restrooms | 3 | 1 | 23-Jan-15 A | 26-Jan-15 | 33 |
| MPT-1104 | (B) Install alcoves, east (Elev. 7/8) | 2 | 1 | 23-Jan-15 A | 26-Jan-15 | 49 |
| L06-8422 | Floor prep | 1 | 0 | 23-Jan-15 A | 23-Jan-15 A | |
| L04-8418 | Flooring - carpet at Elevator Lobby | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 30 |
| L05-8418 | Flooring - carpet at Elevator Lobby | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 30 |
| L06-8418 | Flooring - carpet at Elevator Lobby | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 30 |
| CO-7102T | Cx - DDC Point-To-Point - Central Plant | 5 | 5 | 26-Jan-15 | 30-Jan-15 | 56 |
| L03-7034 | Install doors & hardware (x42) | 1 | 1 | 26-Jan-15* | 26-Jan-15 | 29 |
| L03-7134 | Flooring - VCT | 1 | 1 | 26-Jan-15* | 26-Jan-15 | 27 |
| L11-7032 | Flooring - VCT (x42) | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 27 |
| L04-7138 | Electrical trim & finish | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 32 |
| L05-7138 | Electrical trim & finish | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 32 |
| L06-7138 | Electrical trim & finish | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 32 |
| L07-7138 | Electrical trim & finish | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 32 |

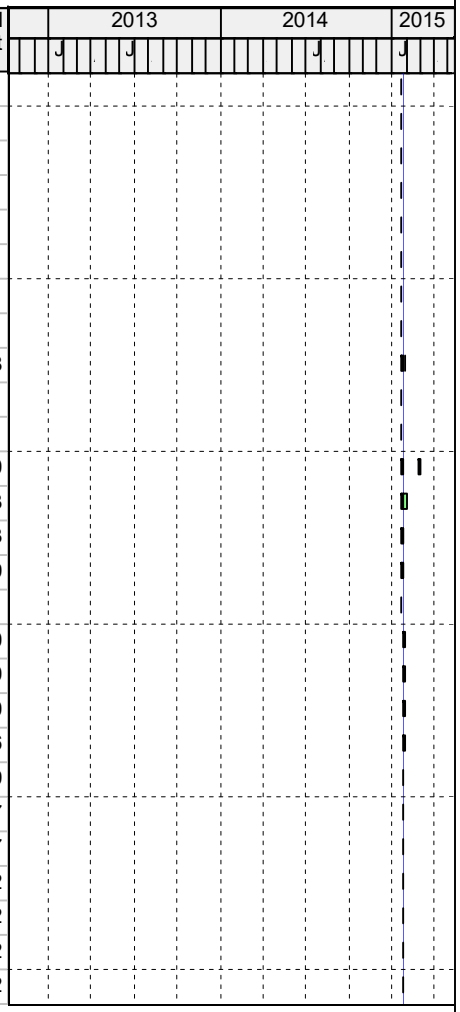



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7138 | Electrical trim & finish | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 32 |
| L09-7138 | Electrical trim & finish | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 32 |
| L10-7138 | Electrical trim & finish | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 32 |
| CO-7216 | Cx - Start-Up Fluid Cooler (power, pre-start & start) | 3 | 3 | 26-Jan-15* | 28-Jan-15 | 33 |
| L16-8140 | Install window sills | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 31 |
| L05-8224 | HVAC grilles & registers at corridors | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 32 |
| L03-8224 | HVAC grilles & registers at corridors | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 30 |
| L04-8224 | HVAC grilles & registers at corridors | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 32 |
| I-1640 | Manlift finishes - Install window sills | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 57 |
| EL-1236 | Elev 1&2 - Walsh/TKE pre-inspection | 6 | 6 | 26-Jan-15 | 02-Feb-15 | 27 |
| MPT-1050 | (B) Install louvers, east | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 51 |
| MPT-1060 | (A) Elevation 33/34 hat channel (east elevation, soutl | 3 | 3 | 26-Jan-15 | 28-Jan-15 | 18 |
| MPT-1090 | Caulking - Elevation 40 (pool south elevation, L3-L17 | 9 | 9 | 26-Jan-15 | 05-Feb-15 | 49 |
| L02-8148 | Paint at Locker Rooms | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 25 |
| L1L-8226 | GWB hang ceilings & complete walls | 3 | 3 | 26-Jan-15 | 28-Jan-15 | 5 |
| LL1-8123 | Floor prep | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 20 |
| SW-2230 | Zone 2 - Repair sidewalk north of 3rd Ave | 5 | 5 | 26-Jan-15 | 30-Jan-15 | 27 |
| SW-2052 | Zone 4 - Waterproof NW planter walls | 4 | 4 | 26-Jan-15 | 29-Jan-15 | 20 |
| LL2-8146 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 26-Jan-15 | 28-Jan-15 | 18 |
| L1B-8138 | GWB hang, tape & finish ceilings at corridors | 11 | 11 | 26-Jan-15 | 09-Feb-15 | 13 |
| L10-8131 | Bathrooms - Install access panels | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 51 |
| L06-8226 | Install base at corridors | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 30 |
| I-5372 | (S) Elevation 32, complete insulation | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 18 |
| GB410-104 | Complete vinyl wallcoverings - Levels 4-10 | 4 | 4 | 26-Jan-15 | 29-Jan-15 | 28 |
| GB1117-100 | Complete GWB - Levels 3, 11-17 | 7 | 7 | 26-Jan-15 | 03-Feb-15 | 29 |
| LL1-Z2-8158 | Wall coverings - vinyl at Meeting Rooms | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 25 |
| L07-8422 | Floor prep | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 24 |

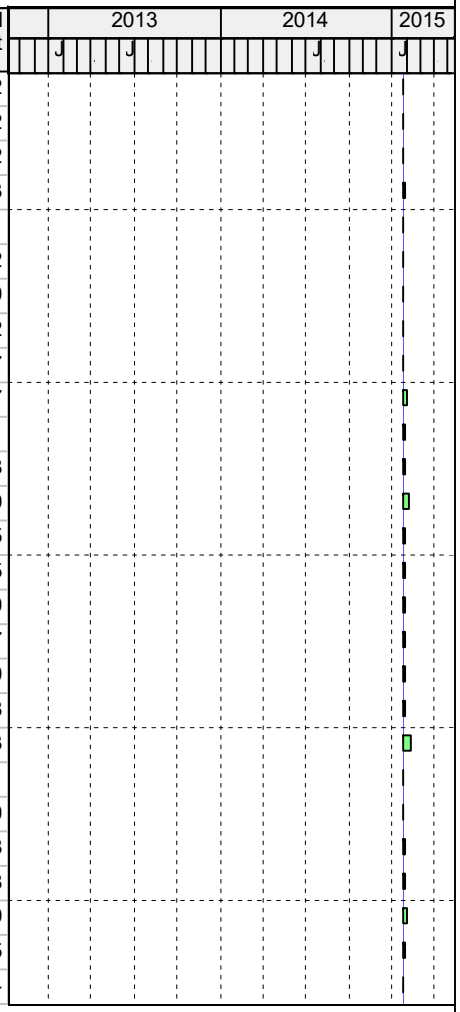


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-5124 | Dining feature wall - install plywood backing | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 0 |
| SW-2322 | Zone 3 - FRP landscape curb at exit door | 5 | 5 | 26-Jan-15 | 30-Jan-15 | 33 |
| L03-7136 | Install doors & hardware | 2 | 2 | 27-Jan-15 | 28-Jan-15 | 27 |
| L16-7034 | Install doors & hardware (x42) | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 28 |
| L17-7032 | Flooring - VCT (x42) | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 27 |
| L04-7134 | Flooring - VCT | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 27 |
| L11-7138 | Electrical trim & finish | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 48 |
| L12-7138 | Electrical trim & finish | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 48 |
| L14-7138 | Electrical trim & finish | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 48 |
| L15-7138 | Electrical trim & finish | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 51 |
| L16-7136 | Install doors & hardware | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 48 |
| L16-7138 | Electrical trim & finish | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 48 |
| LL1-Z3-8142 | Ceramic tile in restrooms | 7 | 7 | 27-Jan-15 | 04-Feb-15 | 33 |
| L16-8224 | HVAC grilles & registers at corridors | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 33 |
| L15-8224 | HVAC grilles & registers at corridors | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 32 |
| L14-8224 | HVAC grilles & registers at corridors | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 32 |
| L12-8224 | HVAC grilles & registers at corridors | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 31 |
| L11-8224 | HVAC grilles & registers at corridors | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 30 |
| LL1-Z3-6036 | GWB hang, tape & finish ceiling at Food Prep (Dry St | 9 | 9 | 27-Jan-15 | 06-Feb-15 | 19 |
| L1L-8272 | GWB hang ceilings | 3 | 3 | 27-Jan-15 | 29-Jan-15 | 13 |
| I-5472 | Reframe Laundry Room ceiling (per ceiling height RF | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 18 |
| L1L-8290 | GWB, top rock | 3 | 3 | 27-Jan-15 | 29-Jan-15 | 0 |
| L11-8131 | Bathrooms - Install access panels | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 51 |
| L08-8226 | Install base at corridors | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 30 |
| MPT-1106 | (B) Install alcoves, north | 3 | 3 | 27-Jan-15 | 29-Jan-15 | 49 |
| I-5478 | Demo existing Laundry Room ceiling | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 18 |
| L08-8422 | Floor prep | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 24 |

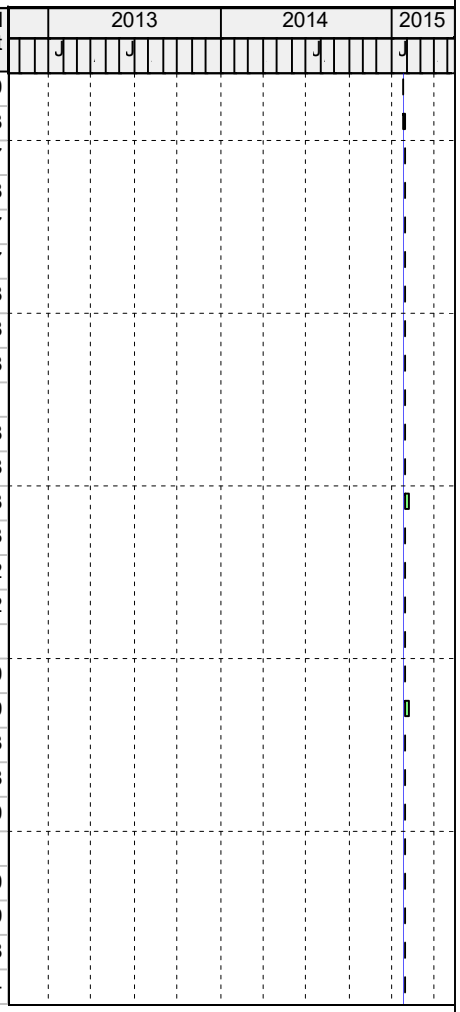



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-5166 | ASI 63 electrical revisions - insulation | 2 | 2 | 27-Jan-15 | 28-Jan-15 | 1 |
| L04-8408 | Install base at Elevator Lobby | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 30 |
| L05-8408 | Install base at Elevator Lobby | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 30 |
| L06-8408 | Install base at Elevator Lobby | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 30 |
| L07-8418 | Flooring - carpet at Elevator Lobby | 2 | 2 | 28-Jan-15 | 29-Jan-15 | 28 |
| L08-8418 | Flooring - carpet at Elevator Lobby | 2 | 2 | 28-Jan-15 | 29-Jan-15 | 28 |
| L17-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 2 | 28-Jan-15 | 29-Jan-15 | 28 |
| L17-7034 | Install doors & hardware (x42) | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 27 |
| L05-7134 | Flooring - VCT | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 27 |
| L17-7136 | Install doors & hardware | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 48 |
| L07-8224 | HVAC grilles & registers at corridors | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 30 |
| L06-8224 | HVAC grilles & registers at corridors | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 30 |
| EL-6042 | Elev 6 - Install EMR heat pump | 6 | 6 | 28-Jan-15 | 04-Feb-15 | 39 |
| CO-7139 | Install remaining devices & prep devices for testing - | 7 | 7 | 28-Jan-15 | 05-Feb-15 | 28 |
| MPT-1038 | (C) Install louvers, north | 5 | 5 | 28-Jan-15 | 02-Feb-15 | 18 |
| MPP-1020 | (C) Elevation 18/19/21/22 & complete 45 (north eleva | 7 | 7 | 28-Jan-15 | 04-Feb-15 | 16 |
| L02-8142 | Ceiling grid at Locker Rooms | 4 | 4 | 28-Jan-15 | 02-Feb-15 | 25 |
| SW-2128 | Zone 1 - FRP planter wall at NE corner | 8 | 8 | 28-Jan-15 | 06-Feb-15 | 28 |
| L12-8131 | Bathrooms - Install access panels | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 51 |
| L14-8226 | Install base at corridors | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 44 |
| I-5373 | (S) Elevation 32, install sign backing | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 15 |
| I-5480 | Revise MEP above Laundry Room ceiling | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 18 |
| L09-8422 | Floor prep | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 24 |
| SW-2130 | Zone 1 - Waterproof wall | 2 | 2 | 28-Jan-15 | 29-Jan-15 | 33 |
| CO-7100T | Cx - Start-Up - Life Safety Exhaust Fans and VFD's | 13 | 13 | 29-Jan-15 | 16-Feb-15 | 28 |
| L03-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 29-Jan-15 | 29-Jan-15 | 27 |
| L03-7138 | Electrical trim & finish | 1 | 1 | 29-Jan-15 | 29-Jan-15 | 46 |

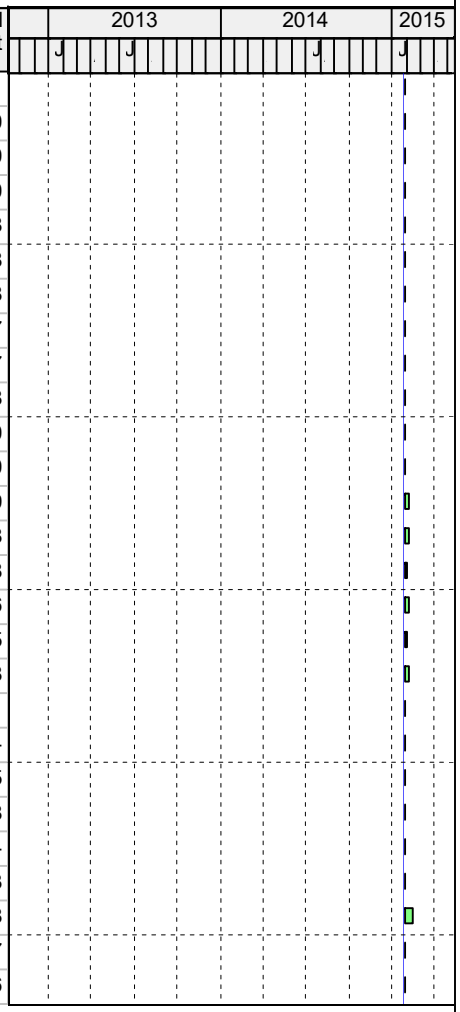


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 1 | 29-Jan-15 | 29-Jan-15 | 27 |
| L04-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 29-Jan-15 | 29-Jan-15 | 27 |
| L05-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 29-Jan-15 | 29-Jan-15 | 27 |
| L06-7134 | Flooring - VCT | 1 | 1 | 29-Jan-15 | 29-Jan-15 | 27 |
| CO-7160 | Generator - Cx generator/owner training | 3 | 3 | 29-Jan-15 | 02-Feb-15 | 67 |
| CO-7400 | Cx - 3rd Party Cx of Mechanical, Plumbing, Electrical | 40 | 40 | 29-Jan-15 | 25-Mar-15 | 30 |
| CO-7218 | Cx - Heat Pump Start-Up - Levels 16 & 17 | 5 | 5 | 29-Jan-15 | 04-Feb-15 | 57 |
| L17-8140 | Install window sills | 1 | 1 | 29-Jan-15 | 29-Jan-15 | 28 |
| CO-7254 | Cx - Start-Up - MUA AAON (8) | 5 | 5 | 29-Jan-15 | 04-Feb-15 | 28 |
| L1L-8228 | GWB tape & finish | 7 | 7 | 29-Jan-15 | 06-Feb-15 | 5 |
| L1L-8248 | Complete electrical/fire alarm rough-in @ ceilings | 3 | 3 | 29-Jan-15 | 02-Feb-15 | 0 |
| L1L-8250 | Complete HVAC RI @ ceilings | 5 | 5 | 29-Jan-15 | 04-Feb-15 | 0 |
| I-5474 | Restore Laundry Room GWB (hang & tape) (per ceili | 5 | 5 | 29-Jan-15 | 04-Feb-15 | 18 |
| LL2-8148 | Fire sprinkler drops to grid | 1 | 1 | 29-Jan-15 | 29-Jan-15 | 18 |
| L02-8154 | Wall coverings - vinyl at north half | 3 | 3 | 29-Jan-15 | 02-Feb-15 | 27 |
| L14-8131 | Bathrooms - Install access panels | 1 | 1 | 29-Jan-15 | 29-Jan-15 | 51 |
| L15-8226 | Install base at corridors | 1 | 1 | 29-Jan-15 | 29-Jan-15 | 44 |
| CO-7140 | Fire Alarm System Device Testing - Tower Levels 4 thı | 7 | 7 | 29-Jan-15 | 06-Feb-15 | 28 |
| L10-8422 | Floor prep | 1 | 1 | 29-Jan-15 | 29-Jan-15 | 24 |
| I-5152 | Sprinkler pipe furring - install framing around pipe | 2 | 2 | 29-Jan-15 | 30-Jan-15 | 1 |
| I-5168 | ASI 63 electrical revisions - vapor barrier | 2 | 2 | 29-Jan-15 | 30-Jan-15 | 1 |
| L07-8408 | Install base at Elevator Lobby | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 28 |
| L08-8408 | Install base at Elevator Lobby | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 28 |
| L09-8418 | Flooring - carpet at Elevator Lobby | 2 | 2 | 30-Jan-15 | 02-Feb-15 | 26 |
| L10-8418 | Flooring - carpet at Elevator Lobby | 2 | 2 | 30-Jan-15 | 02-Feb-15 | 26 |
| L06-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 27 |
| L07-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 27 |

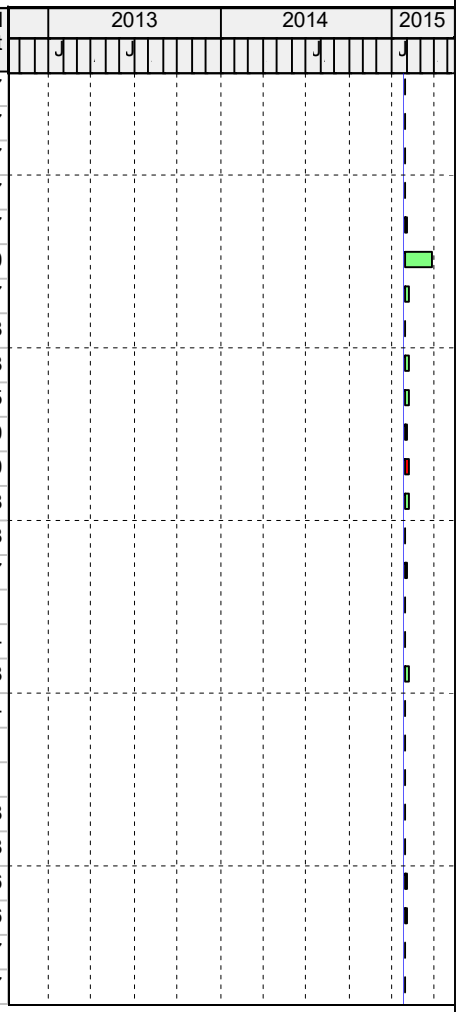



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 27 |
| L08-7134 | Flooring - VCT | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 27 |
| L17-7138 | Electrical trim & finish | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 45 |
| L17-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 30 |
| LL1-8124a | Install base | 10 | 10 | 30-Jan-15 | 12-Feb-15 | 18 |
| L17-8224 | HVAC grilles & registers at corridors | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 30 |
| L08-8224 | HVAC grilles & registers at corridors | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 28 |
| CO-7262 | Cx - Start-Up - Electric Unit Heaters | 3 | 3 | 30-Jan-15 | 03-Feb-15 | 52 |
| EL-6040 | Elev 6 - Install machine room controller equipment/hy | 3 | 3 | 30-Jan-15 | 03-Feb-15 | 37 |
| EL-6054 | Elev 6 - Install EMR doors, hardware & labeling | 2 | 2 | 30-Jan-15 | 02-Feb-15 | 40 |
| L17-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 28 |
| LL1-8160 | Flooring - carpet | 10 | 10 | 30-Jan-15 | 12-Feb-15 | 18 |
| L1K-8144 | Paint, prime & first coat finish | 3 | 3 | 30-Jan-15 | 03-Feb-15 | 16 |
| L1L-8274 | GWB tape & finish walls & ceilings | 7 | 7 | 30-Jan-15 | 09-Feb-15 | 13 |
| SW-2054 | Zone 4 - Install flag pole bases | 3 | 3 | 30-Jan-15 | 03-Feb-15 | 20 |
| L1B-6015 | HVAC drops at West Ballrooms | 5 | 5 | 30-Jan-15 | 05-Feb-15 | 0 |
| L1B-6021 | Electrical drops at West Ballrooms | 5 | 5 | 30-Jan-15 | 05-Feb-15 | 0 |
| L1B-6023 | Fire sprinkler drops at West Ballrooms | 5 | 5 | 30-Jan-15 | 05-Feb-15 | 0 |
| L15-8131 | Bathrooms - Install access panels | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 51 |
| L16-8226 | Install base at corridors | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 44 |
| MPP-1052 | (B) Elevation 3 (south elevation, west of manlift, L1-L | 5 | 5 | 30-Jan-15 | 04-Feb-15 | 49 |
| GB410-108 | Complete base - Levels 4-10 | 4 | 4 | 30-Jan-15 | 04-Feb-15 | 29 |
| GB410-110 | Complete countertops - Levels 4-10 | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 28 |
| GB410-112 | Complete shower/tub surrounds - Levels 4-10 | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 28 |
| L03-8422 | Floor prep | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 24 |
| L09-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 27 |
| L10-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 27 |

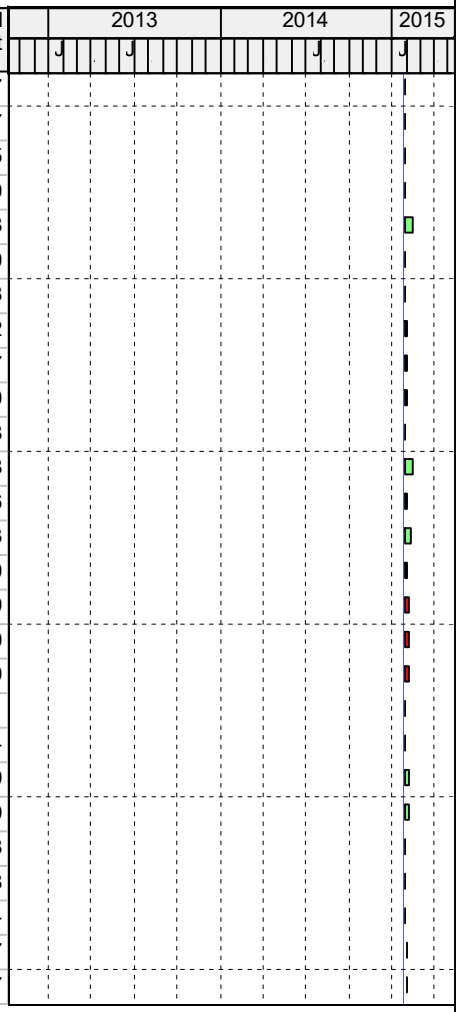



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 42 |
| L02-8130 | Ceiling grid at south half | 5 | 5 | 02-Feb-15 | 06-Feb-15 | 21 |
| CO-7232 | Cx - TAB - CW Pump Totalization | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 45 |
| LL1-6014Id | L1 bar redesign - paint ceilings at Excercise & MR9 | 2 | 2 | 02-Feb-15 | 03-Feb-15 | 19 |
| L17-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 31 |
| LL1-Z3-FCC28 | Electrical trim & finish at FCC | 4 | 4 | 02-Feb-15 | 05-Feb-15 | 26 |
| L16-8131 | Bathrooms - Install access panels | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 51 |
| L17-8226 | Install base at corridors | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 44 |
| GB410-114 | Complete plumbing fixture installation - Levels 4-10 | 3 | 3 | 02-Feb-15 | 04-Feb-15 | 28 |
| L11-8422 | Floor prep | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 24 |
| I-5154 | Sprinkler pipe furring - GWB hang, tape & finish | 7 | 7 | 02-Feb-15 | 10-Feb-15 | 1 |
| I-5170 | ASI 63 electrical revisions - GWB hang, tape & finish | 7 | 7 | 02-Feb-15 | 10-Feb-15 | 1 |
| SW-2234 | Zone 2 - FRP door curbs | 4 | 4 | 02-Feb-15 | 05-Feb-15 | 27 |
| L09-8408 | Install base at Elevator Lobby | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 26 |
| L10-8408 | Install base at Elevator Lobby | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 26 |
| L11-8418 | Flooring - carpet at Elevator Lobby | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 25 |
| L12-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 42 |
| L14-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 42 |
| L15-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 42 |
| L09-7134 | Flooring - VCT | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 26 |
| L10-7134 | Flooring - VCT | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 26 |
| L1L-8102a | GWB tape & finish walls & ceilings | 7 | 7 | 03-Feb-15 | 11-Feb-15 | 0 |
| CO-7234 | Cx - TAB - CW Water Balancing | 10 | 10 | 03-Feb-15 | 16-Feb-15 | 45 |
| L10-8224 | HVAC grilles & registers at corridors | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 26 |
| L09-8224 | HVAC grilles & registers at corridors | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 26 |
| MPT-1056 | (A) Complete Elevation 31 (above L12 terrace, west e | 3 | 3 | 03-Feb-15 | 05-Feb-15 | 18 |
| MPT-1070 | Tower Sign, East (El. 44) | 5 | 5 | 03-Feb-15 | 09-Feb-15 | 42 |

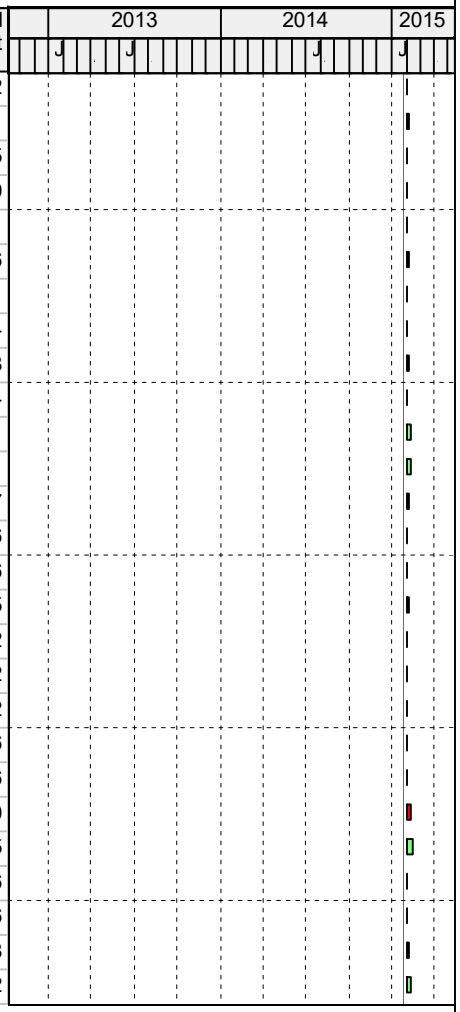


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPT-1098 | Caulking - Elevation 30 (south elevation, west of man | 6 | 6 | 03-Feb-15 | 10-Feb-15 | 46 |
| L02-8145 | MEP drops to framed ceiling (including inspections) | 4 | 4 | 03-Feb-15 | 06-Feb-15 | 25 |
| L1L-8246 | Complete fire sprinkler RI @ ceilings | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 0 |
| L02-8156 | Install doors & hardware at north half | 3 | 3 | 03-Feb-15 | 05-Feb-15 | 34 |
| L02-8158 | Ceiling grid at north half | 3 | 3 | 03-Feb-15 | 05-Feb-15 | 27 |
| L17-8131 | Bathrooms - Install access panels | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 51 |
| L12-8422 | Floor prep | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 24 |
| MPT-1120 | Cap metal at L12 Terrace | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 40 |
| L16-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 04-Feb-15 | 04-Feb-15 | 42 |
| L17-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 04-Feb-15 | 04-Feb-15 | 42 |
| L1K-8102a | GWB hang ceilings at Public Restroom | 2 | 2 | 04-Feb-15 | 05-Feb-15 | 8 |
| CO-7226 | Cx - Start-Up - Misc. Equipment | 5 | 5 | 04-Feb-15 | 10-Feb-15 | 52 |
| EL-6044 | Elev 6 - Electrical trim & finish | 3 | 3 | 04-Feb-15 | 06-Feb-15 | 37 |
| EL-6046 | Elev 6 - Fire alarm trim | 3 | 3 | 04-Feb-15 | 06-Feb-15 | 37 |
| EL-6048 | Elev 6 - Fire sprinkler trim | 3 | 3 | 04-Feb-15 | 06-Feb-15 | 37 |
| EL-6050 | Elev 6 - Install pit grates | 3 | 3 | 04-Feb-15 | 06-Feb-15 | 37 |
| LL1-6014Id2 | L1 bar redesign - install wall coverings at MR9 | 3 | 3 | 04-Feb-15 | 06-Feb-15 | 19 |
| L1K-8136 | Ceiling grid & inspection | 4 | 4 | 04-Feb-15 | 09-Feb-15 | 16 |
| L1K-8152 | Install doors & hardware | 3 | 3 | 04-Feb-15 | 06-Feb-15 | 24 |
| LL1-8172 | Ceiling grid & inspection at Exercise Room | 2 | 2 | 04-Feb-15 | 05-Feb-15 | 23 |
| LL1-8184 | Install storefront at Exercise Room | 1 | 1 | 04-Feb-15 | 04-Feb-15 | 24 |
| L1K-8162 | Complete wallcoverings (FRP) | 2 | 2 | 04-Feb-15 | 05-Feb-15 | 23 |
| GB1117-102 | Complete painting - Levels 3, 11-17 | 3 | 3 | 04-Feb-15 | 06-Feb-15 | 29 |
| LL4-8136 | Clear out and clean parking area | 10 | 10 | 04-Feb-15 | 17-Feb-15 | 35 |
| LL3-8136 | Clear out and clean parking area | 10 | 10 | 04-Feb-15 | 17-Feb-15 | 35 |
| L14-8422 | Floor prep | 1 | 1 | 04-Feb-15 | 04-Feb-15 | 36 |
| L11-8408 | Install base at Elevator Lobby | 1 | 1 | 05-Feb-15 | 05-Feb-15 | 41 |

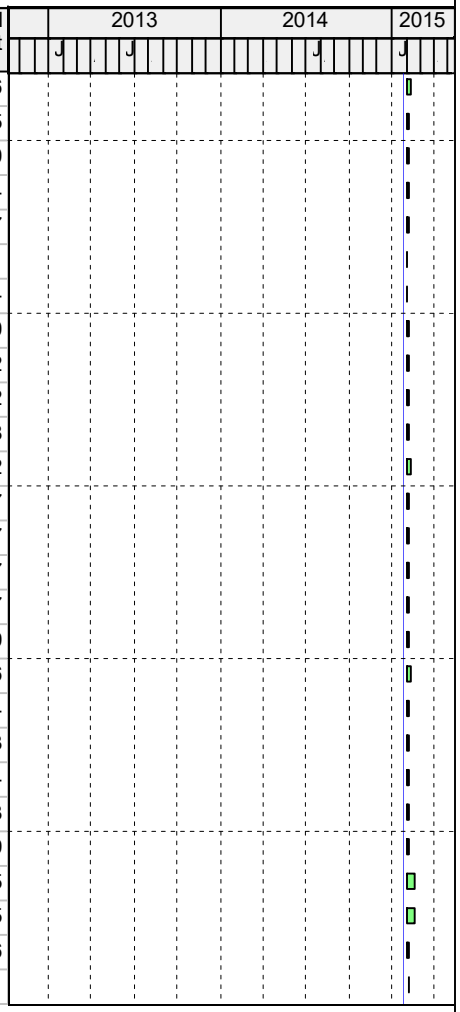



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8418 | Flooring - carpet at Elevator Lobby | 2 | 2 | 05-Feb-15 | 06-Feb-15 | 23 |
| L11-7134 | Flooring - VCT | 1 | 1 | 05-Feb-15 | 05-Feb-15 | 36 |
| CO-7256 | Cx - Start-Up - Elevator Machine Room Ductless Split | 1 | 1 | 05-Feb-15 | 05-Feb-15 | 34 |
| CO-7258 | Cx - Start-Up - KMUA Trane (2) | 2 | 2 | 05-Feb-15 | 06-Feb-15 | 28 |
| CO-7404 | Cx - FPT - Heat Pumps | 3 | 3 | 05-Feb-15 | 09-Feb-15 | 57 |
| L1L-8218 | Frame ceilings & inspection | 5 | 5 | 05-Feb-15 | 11-Feb-15 | 0 |
| L1L-8256 | GWB hang walls | 3 | 3 | 05-Feb-15 | 09-Feb-15 | 2 |
| I-5476 | Repaint Laundry Room ceiling | 1 | 1 | 05-Feb-15 | 05-Feb-15 | 18 |
| LL1-8156 | Install doors & hardware at corridors | 2 | 2 | 05-Feb-15 | 06-Feb-15 | 25 |
| LL1-8182 | Install doors & hardware at Exercise Room | 1 | 1 | 05-Feb-15 | 05-Feb-15 | 24 |
| MPP-1054 | Caulking - Elevation 3 (south elevation, west of manli | 3 | 3 | 05-Feb-15 | 09-Feb-15 | 47 |
| GB410-116 | Complete shower doors - Levels 4-10 | 2 | 2 | 05-Feb-15 | 06-Feb-15 | 28 |
| GB410-118 | Complete barn doors - Levels 4-10 | 1 | 1 | 05-Feb-15 | 05-Feb-15 | 29 |
| MPP-1062 | (C) Install level 3 cornice metal (Porte Cochere) | 2 | 2 | 05-Feb-15 | 06-Feb-15 | 16 |
| L15-8422 | Floor prep | 1 | 1 | 05-Feb-15 | 05-Feb-15 | 36 |
| LL1-Z3-8156 | Install countertops at restrooms | 2 | 2 | 05-Feb-15 | 06-Feb-15 | 33 |
| LL1-Z3-8158 | Install toilet partitions | 4 | 4 | 05-Feb-15 | 10-Feb-15 | 37 |
| MPT-1118 | Cap metal - Pool terrace | 3 | 3 | 05-Feb-15 | 09-Feb-15 | 38 |
| LL1-Z3-8160 | Install doors & hardware at restrooms | 2 | 2 | 05-Feb-15 | 06-Feb-15 | 38 |
| LL2-2062 | Ceiling grid at Laundry | 3 | 3 | 06-Feb-15 | 10-Feb-15 | 18 |
| MPT-1018a | (A) Install hi-roof cornice metal | 8 | 8 | 06-Feb-15 | 14-Feb-15 | 18 |
| SW-2212 | Zone 2 - FRP sidewalk panels | 2 | 2 | 06-Feb-15 | 09-Feb-15 | 27 |
| LL1-Z3-FCC30 | Data/phone trim/finish at FCC | 4 | 4 | 06-Feb-15 | 11-Feb-15 | 26 |
| L1K-8102b | GWB tape & finish at Restrooms | 7 | 7 | 06-Feb-15 | 16-Feb-15 | 8 |
| MPT-1092 | Caulking - Elevation 31 (above L12 terrace, west elev | 4 | 4 | 06-Feb-15 | 11-Feb-15 | 39 |
| CO-7139.1 | Install remaining devices & prep devices for testing - | 6 | 6 | 06-Feb-15 | 13-Feb-15 | 28 |
| SW-2222 | Zone 2 - Install j-box at NE corner | 1 | 1 | 06-Feb-15 | 06-Feb-15 | 27 |

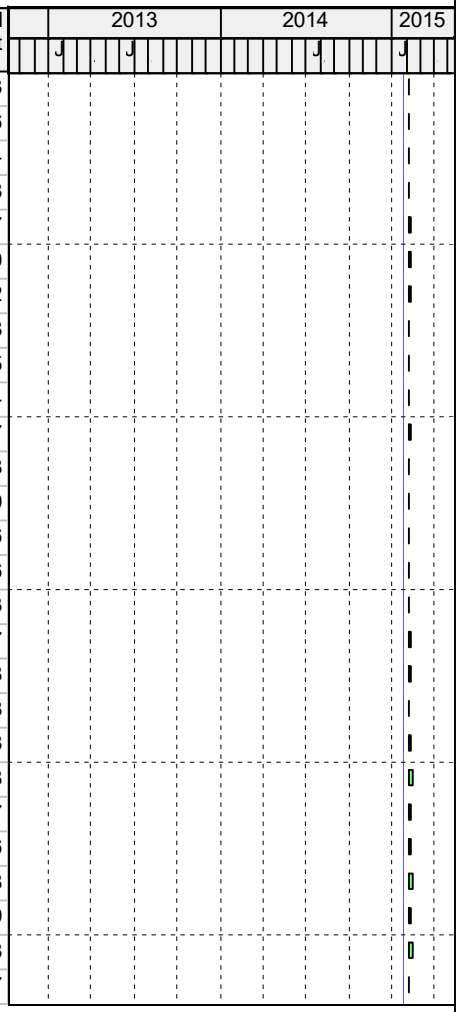



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-8174 | Wall coverings - vinyl at Exercise Room | 2 | 2 | 06-Feb-15 | 09-Feb-15 | 24 |
| LL1-8176 | HVAC drops/trim to grid | 1 | 1 | 06-Feb-15 | 06-Feb-15 | 23 |
| L1B-6011 | GWB, hang ceiling at West Ballrooms | 4 | 4 | 06-Feb-15 | 11-Feb-15 | 3 |
| L1B-6029 | HVAC drops at East Ballroom | 5 | 5 | 06-Feb-15 | 12-Feb-15 | 0 |
| L1B-6031 | Electrical drops at East Ballroom | 5 | 5 | 06-Feb-15 | 12-Feb-15 | 0 |
| L1B-6033 | Fire sprinkler drops at East Ballroom | 5 | 5 | 06-Feb-15 | 12-Feb-15 | 0 |
| L02-8160 | HVAC drops/trim at north half | 2 | 2 | 06-Feb-15 | 09-Feb-15 | 27 |
| L16-8422 | Floor prep | 1 | 1 | 06-Feb-15 | 06-Feb-15 | 36 |
| I-5132 | Bar plumbing relocation - relocate waste line | 3 | 3 | 06-Feb-15 | 10-Feb-15 | 10 |
| MPP-1050 | (C) Columns at Porte Cochere | 4 | 4 | 07-Feb-15 | 11-Feb-15 | 16 |
| L12-8408 | Install base at Elevator Lobby | 1 | 1 | 09-Feb-15 | 09-Feb-15 | 39 |
| L14-8418 | Flooring - carpet at Elevator Lobby | 2 | 2 | 09-Feb-15 | 10-Feb-15 | 38 |
| L03-8622 | HVAC trim at Pool | 2 | 2 | 09-Feb-15 | 10-Feb-15 | 2 |
| L03-8624 | Fire sprinkler trim at Pool | 2 | 2 | 09-Feb-15 | 10-Feb-15 | 4 |
| CO-7116T | Fire Alarm Pre-Testing (Tower) - Tower Levels 4 thru 1( | 6 | 6 | 09-Feb-15 | 16-Feb-15 | 28 |
| L12-7134 | Flooring - VCT | 1 | 1 | 09-Feb-15 | 09-Feb-15 | 35 |
| SW-2118 | Zone 1 - FRP sidewalk (NE & SE corners) | 2 | 2 | 09-Feb-15 | 10-Feb-15 | 28 |
| CO-7220 | Cx - Start-Up - Common Space Heat Pump | 4 | 4 | 09-Feb-15 | 12-Feb-15 | 28 |
| LL1-Z3-8144 | Plumbing fixtures & trim at Restrooms | 5 | 5 | 09-Feb-15 | 13-Feb-15 | 33 |
| CO-7260 | Cx - Start-Up - Ballroom AAON RTU | 1 | 1 | 09-Feb-15 | 09-Feb-15 | 42 |
| CO-7138 | Elevator Finals with AHJ | 5 | 5 | 09-Feb-15 | 13-Feb-15 | 42 |
| MPP-1048 | Caulking - Porte Cochere cornice metal | 3 | 3 | 09-Feb-15 | 11-Feb-15 | 45 |
| L02-8150 | Install doors & hardware at Locker Rooms | 1 | 1 | 09-Feb-15 | 09-Feb-15 | 25 |
| LL1-Z3-8120 | Wall coverings - vinyl | 4 | 4 | 09-Feb-15 | 12-Feb-15 | 22 |
| L1K-8124a2 | Install doors & hardware | 2 | 2 | 09-Feb-15 | 10-Feb-15 | 15 |
| L1L-8230 | Paint, prime & first coat finish | 3 | 3 | 09-Feb-15 | 11-Feb-15 | 5 |
| LL1-8178 | Lighting & electrical drops to grid | 2 | 2 | 09-Feb-15 | 10-Feb-15 | 23 |

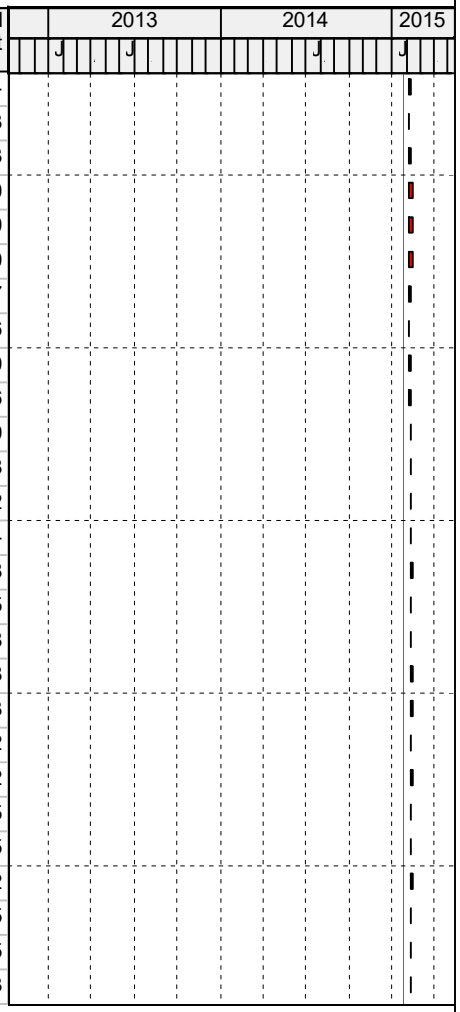



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-8180 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 09-Feb-15 | 10-Feb-15 | 23 |
| LL1-Z3-6038 | Paint ceiling at Food Prep (Dry Storage) | 2 | 2 | 09-Feb-15 | 10-Feb-15 | 19 |
| GB1117-104 | Complete vinyl wallcoverings - Levels 3, 11-17 | 5 | 5 | 09-Feb-15 | 13-Feb-15 | 29 |
| GB1117-106 | Complete flooring - Levels 3, 11-17 | 4 | 4 | 09-Feb-15 | 12-Feb-15 | 30 |
| CO-7140.1 | Fire Alarm System Device Testing - Tower Levels 3, 1' | 6 | 6 | 09-Feb-15 | 16-Feb-15 | 28 |
| L17-8422 | Floor prep | 1 | 1 | 09-Feb-15 | 09-Feb-15 | 36 |
| I-5142 | Damper at BPF #8 - mechanical revisions | 2 | 2 | 09-Feb-15 | 10-Feb-15 | 3 |
| SW-2058 | Zone 4 - Demo existing curb at 110th | 1 | 1 | 09-Feb-15 | 09-Feb-15 | 17 |
| CM-1024 | Tower - "Clean/Punch" Complete - All Floors | 0 | 0 | | 09-Feb-15 | 27 |
| L1BOH2-8104 | Paint, prime | 2 | 2 | 10-Feb-15 | 11-Feb-15 | 14 |
| L14-7134 | Flooring - VCT | 1 | 1 | 10-Feb-15 | 10-Feb-15 | 35 |
| CO-7264 | Cx - Start-Up - Lobby Trane TRU (2) | 2 | 2 | 10-Feb-15 | 11-Feb-15 | 50 |
| CO-7132 | Cx - DDC Point-To-Point - Ballroom VAV | 1 | 1 | 10-Feb-15 | 10-Feb-15 | 42 |
| SW-2022 | Zone 4 - Remove pedestrian protection on 110th Ave | 1 | 1 | 10-Feb-15 | 10-Feb-15 | 17 |
| L1K-8150 | HVAC drops/trim at ceiling | 2 | 2 | 10-Feb-15 | 11-Feb-15 | 16 |
| L1L-8276 | Paint, prime & first coat finish | 3 | 3 | 10-Feb-15 | 12-Feb-15 | 13 |
| LL1-Z2-8144 | Install doors & hardware at corridors | 2 | 2 | 10-Feb-15 | 11-Feb-15 | 30 |
| L1B-8142 | Paint, prime & first coat finish walls & ceilings at corrid | 2 | 2 | 10-Feb-15 | 11-Feb-15 | 13 |
| L02-8162 | Lighting & electrical trim at north half | 3 | 3 | 10-Feb-15 | 12-Feb-15 | 27 |
| L02-8164 | Fire alarm trim (speaker/strobe & smoke detector bas | 3 | 3 | 10-Feb-15 | 12-Feb-15 | 27 |
| MPT-1114 | Cap metal - Porte Cochere | 3 | 3 | 10-Feb-15 | 12-Feb-15 | 38 |
| L14-8408 | Install base at Elevator Lobby | 1 | 1 | 11-Feb-15 | 11-Feb-15 | 38 |
| L15-8418 | Flooring - carpet at Elevator Lobby | 2 | 2 | 11-Feb-15 | 12-Feb-15 | 38 |
| LL1-Z2-8118a | Install decorative light fixtures | 3 | 3 | 11-Feb-15 | 13-Feb-15 | 15 |
| LL2-2094 | Install doors & hardware at Laundry | 2 | 2 | 11-Feb-15 | 12-Feb-15 | 25 |
| CO-7134 | Cx - DDC Point-To-Point - Ballroom RTU (2) | 2 | 2 | 11-Feb-15 | 12-Feb-15 | 42 |
| SW-2032 | Zone 4 - Demo existing trees & hardscapes | 3 | 3 | 11-Feb-15 | 13-Feb-15 | 17 |

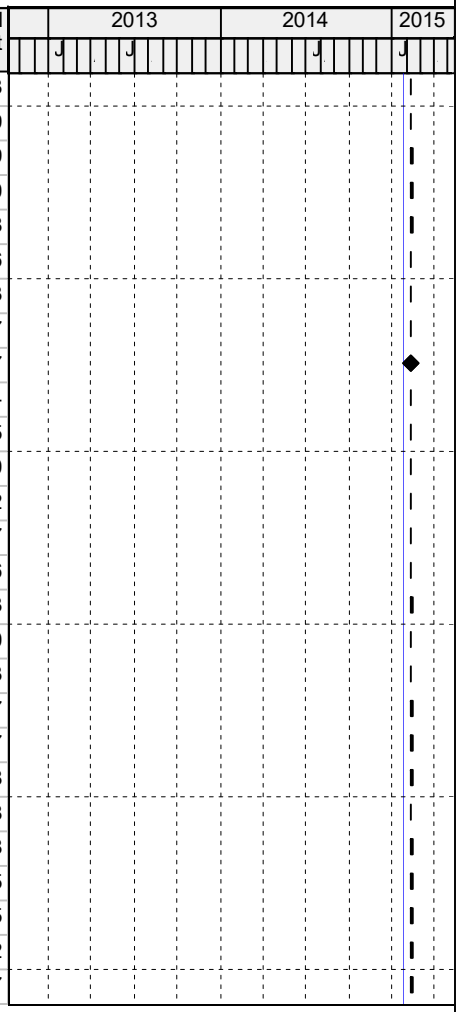



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8666 | Electrical trim & finish at ceiling at Pool | 2 | 2 | 11-Feb-15 | 12-Feb-15 | 2 |
| L02-8140 | Lighting & electrical trim at south half | 3 | 3 | 11-Feb-15 | 13-Feb-15 | 21 |
| LL1-8128 | Floor prep at Exercise Room | 2 | 2 | 11-Feb-15 | 12-Feb-15 | 23 |
| L1K-8130 | HVAC drops/trim at celing | 2 | 2 | 11-Feb-15 | 12-Feb-15 | 9 |
| SW-2320 | Zone 3 - Pour ped pole base | 3 | 3 | 11-Feb-15 | 13-Feb-15 | 28 |
| LL2-2098 | HVAC drops to grid at Laundry | 2 | 2 | 11-Feb-15 | 12-Feb-15 | 22 |
| LL1-8186 | Wall coverings - vinyl at corridors | 5 | 5 | 11-Feb-15 | 17-Feb-15 | 18 |
| LL1-Z2-8122 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 11-Feb-15 | 13-Feb-15 | 15 |
| LL1-Z3-8206 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 11-Feb-15 | 13-Feb-15 | 19 |
| LL2-2106 | Floor prep | 2 | 2 | 11-Feb-15 | 12-Feb-15 | 18 |
| I-5134 | Bar plumbing relocation - adust framing | 1 | 1 | 11-Feb-15 | 11-Feb-15 | 10 |
| I-5144 | Damper at BPF #8 - framing revisions | 1 | 1 | 11-Feb-15 | 11-Feb-15 | 3 |
| L1BOH2-8200 | Paint, first coat finish | 1 | 1 | 12-Feb-15 | 12-Feb-15 | 14 |
| CO-7228 | Cx - Start-Up - Poolpak | 1 | 1 | 12-Feb-15 | 12-Feb-15 | 50 |
| SW-2046 | Zone 4 - Install conduit | 2 | 2 | 12-Feb-15 | 13-Feb-15 | 17 |
| LL1-Z3-FCC32 | Flooring - VCT at FCC | 3 | 3 | 12-Feb-15 | 16-Feb-15 | 26 |
| L1K-8148 | Lighting & electrical trim at ceiling | 2 | 2 | 12-Feb-15 | 13-Feb-15 | 16 |
| L1L-8232 | Wall coverings - vinyl | 5 | 5 | 12-Feb-15 | 18-Feb-15 | 28 |
| L1K-8164 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 12-Feb-15 | 13-Feb-15 | 16 |
| L1B-8102a | GWB, tape & finish ceiling at West Ballroom | 7 | 7 | 12-Feb-15 | 20-Feb-15 | 3 |
| L1B-8162 | Install doors & hardware at corridors | 2 | 2 | 12-Feb-15 | 13-Feb-15 | 22 |
| L1L-8292 | GWB hang ceilings | 4 | 4 | 12-Feb-15 | 17-Feb-15 | 0 |
| MPP-1018 | (C) Elevation A/B/C (Porte Cochere wall panels) | 2 | 2 | 12-Feb-15 | 13-Feb-15 | 16 |
| L1L-8310 | Install 9-wood ceiling supports at Sitting Area | 2 | 2 | 12-Feb-15 | 13-Feb-15 | 5 |
| I-5136 | Bar plumbing relocation - GWB hang, tape & finish | 7 | 7 | 12-Feb-15 | 20-Feb-15 | 10 |
| I-5146 | Damper at BPF #8 - complete GWB hang | 1 | 1 | 12-Feb-15 | 12-Feb-15 | 3 |
| L1BOH2-8114 | Ceiling grid & inspection | 4 | 4 | 13-Feb-15 | 18-Feb-15 | 14 |

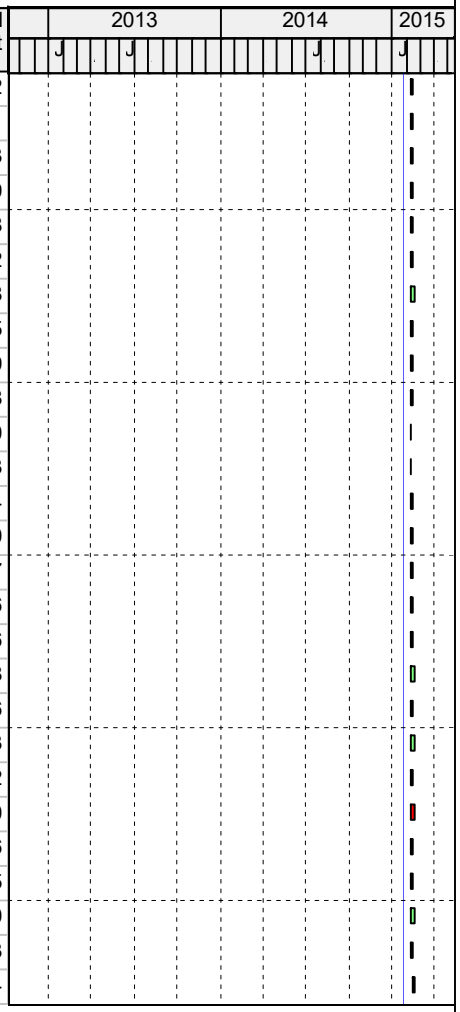



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8408 | Install base at Elevator Lobby | 1 | 1 | 13-Feb-15 | 13-Feb-15 | 38 |
| L16-8418 | Flooring - carpet at Elevator Lobby | 2 | 2 | 13-Feb-15 | 16-Feb-15 | 33 |
| L15-7134 | Flooring - VCT | 1 | 1 | 13-Feb-15 | 13-Feb-15 | 33 |
| LL1-Z2-8124a | Install base | 10 | 10 | 13-Feb-15 | 26-Feb-15 | 24 |
| CO-7224 | Cx - Start-Up - Gravity Relief Ventilator | 1 | 1 | 13-Feb-15 | 13-Feb-15 | 28 |
| LL2-2088 | Lighting & electrical drops to grid at Laundry | 2 | 2 | 13-Feb-15 | 16-Feb-15 | 22 |
| CO-7136 | Cx - DDC Point-To-Point - MUA AAON Start-Up (8) | 5 | 5 | 13-Feb-15 | 19-Feb-15 | 42 |
| SW-2036 | Zone 4 - Grade for curb and gutter | 2 | 2 | 13-Feb-15 | 16-Feb-15 | 17 |
| L03-8668 | Remove scaffolding at pool pit | 1 | 1 | 13-Feb-15 | 13-Feb-15 | 2 |
| L1K-8120 | Lighting & electrical trim at ceiling | 2 | 2 | 13-Feb-15 | 16-Feb-15 | 9 |
| LL1-8130 | Install base | 3 | 3 | 13-Feb-15 | 17-Feb-15 | 23 |
| LL1-8136 | Ceramic tile in restrooms | 3 | 3 | 13-Feb-15 | 17-Feb-15 | 23 |
| LL2-2102 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 13-Feb-15 | 16-Feb-15 | 23 |
| LL1-8154 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 13-Feb-15 | 17-Feb-15 | 18 |
| L1K-8160 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 13-Feb-15 | 16-Feb-15 | 10 |
| L1B-6017 | GWB, hang ceiling at East Ballrooms | 4 | 4 | 13-Feb-15 | 18-Feb-15 | 0 |
| L02-8166 | Fire sprinkler trim at north half | 2 | 2 | 13-Feb-15 | 16-Feb-15 | 27 |
| L02-8168 | Floor prep at north half | 2 | 2 | 13-Feb-15 | 16-Feb-15 | 27 |
| LL2-2104 | Flooring - epoxy at equipment alcoves | 7 | 7 | 13-Feb-15 | 23-Feb-15 | 18 |
| SW-2060 | Zone 4 - Sawcut curb & gutter | 1 | 1 | 13-Feb-15 | 13-Feb-15 | 17 |
| MPP-1064 | (C) Install column at Pool | 1 | 1 | 14-Feb-15 | 14-Feb-15 | 16 |
| CO-7230 | Cx - TAB - Air Balancing | 15 | 15 | 16-Feb-15 | 06-Mar-15 | 28 |
| LL1-Z3-8146 | Install restroom accessories | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 34 |
| SW-2038 | Zone 4 - FRP curb & gutter | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 17 |
| L03-8670 | Rough-in pool trench drain at Pool | 4 | 4 | 16-Feb-15 | 19-Feb-15 | 2 |
| L03-8672 | Prep pool area for topping slab | 4 | 4 | 16-Feb-15 | 19-Feb-15 | 2 |
| MPT-1084 | Caulking - Hi-roof cornice metal | 6 | 6 | 16-Feb-15 | 23-Feb-15 | 37 |

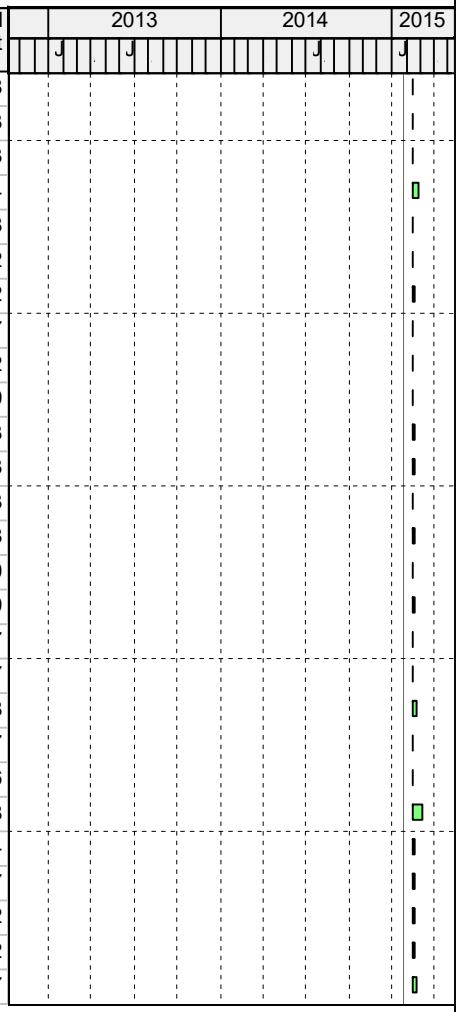



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8146 | Fire sprinkler drops/trim at ceiling | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 16 |
| LL1-Z2-8123 | Floor prep | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 15 |
| SW-2228 | Zone 2 - Pull wire and install light poles | 5 | 5 | 16-Feb-15 | 20-Feb-15 | 23 |
| SW-2232 | Zone 2 - Replace luminaire north of 3rd | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 27 |
| SW-2328 | Zone 3 - Pull wire and install light poles | 5 | 5 | 16-Feb-15 | 20-Feb-15 | 28 |
| LL1-Z2-8128 | HVAC trim at ceiling | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 15 |
| LL1-Z3-8150 | Paint, final coat & touch-up | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 33 |
| LL1-Z3-8154 | Complete MEP trim at Restroom | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 33 |
| L02-8114 | Floor prep at south half | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 21 |
| MPP-1056 | Caulking - Porte Cochere walls & columns | 3 | 3 | 16-Feb-15 | 18-Feb-15 | 40 |
| GB1117-108 | Complete base - Levels 3, 11-17 | 5 | 5 | 16-Feb-15 | 20-Feb-15 | 31 |
| GB1117-110 | Complete countertops - Levels 3, 11-17 | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 31 |
| GB1117-112 | Complete shower/tub surrounds - Levels 3, 11-17 | 3 | 3 | 16-Feb-15 | 18-Feb-15 | 29 |
| LL2-8152 | Clear out and clean parking area | 10 | 10 | 16-Feb-15 | 27-Feb-15 | 21 |
| L1L-8312 | HVAC drops to 9-wood ceiling | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 5 |
| L1L-8314 | Electrical drops to 9-wood ceiling | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 5 |
| L1L-8316 | Fire sprinkler drops to 9-wood ceiling | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 5 |
| MPT-1110 | Cap metal at hi-roof | 5 | 5 | 16-Feb-15 | 20-Feb-15 | 33 |
| L03-8418 | Flooring - carpet at Elevator Lobby | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 31 |
| L16-8408 | Install base at Elevator Lobby | 1 | 1 | 17-Feb-15 | 17-Feb-15 | 33 |
| L17-8418 | Flooring - carpet at Elevator Lobby | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 31 |
| L16-7134 | Flooring - VCT | 1 | 1 | 17-Feb-15 | 17-Feb-15 | 32 |
| RF-4070 | TR - Terrace Roof - Install American Hydrotech assem | 3 | 3 | 17-Feb-15 | 19-Feb-15 | 39 |
| LL1-Z3-FCC34 | Paint, final coat & touch-up up at FCC | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 26 |
| LL1-Z3-FCC36 | Install doors & hardware at FCC | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 26 |
| O-7116T.1 | Fire Alarm Pre-Testing (Tower) - Tower Levels 3, 11 thr | 6 | 6 | 17-Feb-15 | 24-Feb-15 | 28 |
| L1K-8122 | Fire sprinkler drops/trim at ceiling | 1 | 1 | 17-Feb-15 | 17-Feb-15 | 10 |

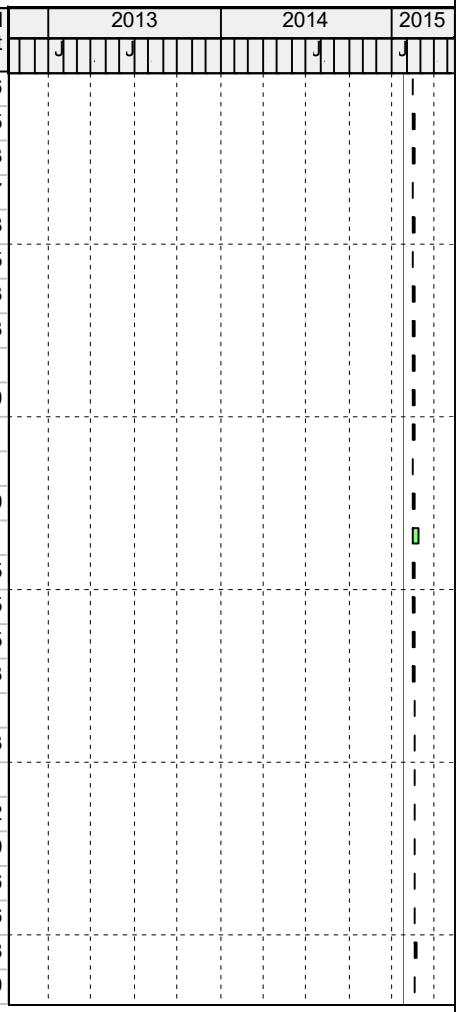



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8123 | Floor prep | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 9 |
| L1K-8125 | Floor prep | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 16 |
| LL2-2100 | Fire sprinkler drops to grid at Laundry | 1 | 1 | 17-Feb-15 | 17-Feb-15 | 22 |
| LL1-Z2-8130 | Fire sprinkler trim | 1 | 1 | 17-Feb-15 | 17-Feb-15 | 15 |
| LL1-Z2-8142 | Wall coverings - vinyl at corridors | 3 | 3 | 17-Feb-15 | 19-Feb-15 | 24 |
| L02-8170 | Flooring - VCT at north half | 3 | 3 | 17-Feb-15 | 19-Feb-15 | 27 |
| SW-2034 | Zone 4 - Install irrigation sleeves | 1 | 1 | 18-Feb-15 | 18-Feb-15 | 17 |
| LL1-8138 | Flooring - install cork floor at Exercise Room | 3 | 3 | 18-Feb-15 | 20-Feb-15 | 23 |
| L1L-8128 | Install die wall at bar | 3 | 3 | 18-Feb-15 | 20-Feb-15 | 2 |
| L1L-8258 | GWB tape & finish walls & ceilings | 7 | 7 | 18-Feb-15 | 26-Feb-15 | 0 |
| LL1-8158 | Floor prep at corridors | 2 | 2 | 18-Feb-15 | 19-Feb-15 | 18 |
| L1B-8144 | Wall coverings - vinyl at corridors | 3 | 3 | 18-Feb-15 | 20-Feb-15 | 17 |
| L1B-8146 | HVAC drops/trim at corridors | 2 | 2 | 18-Feb-15 | 19-Feb-15 | 13 |
| L02-8152 | Flooring - VCT at south half | 2 | 2 | 18-Feb-15 | 19-Feb-15 | 21 |
| L1L-8318 | Install 9-wood ceiling at Sitting Area | 3 | 3 | 18-Feb-15 | 20-Feb-15 | 5 |
| L1BOH2-8126 | Install doors & hardware | 3 | 3 | 19-Feb-15 | 23-Feb-15 | 14 |
| L1BOH2-8204 | HVAC drops/trim at ceiling | 2 | 2 | 19-Feb-15 | 20-Feb-15 | 16 |
| L03-8408 | Install base at Elevator Lobby | 1 | 1 | 19-Feb-15 | 19-Feb-15 | 31 |
| L17-8408 | Install base at Elevator Lobby | 1 | 1 | 19-Feb-15 | 19-Feb-15 | 31 |
| L17-7134 | Flooring - VCT | 1 | 1 | 19-Feb-15 | 19-Feb-15 | 31 |
| L1K-8124a | Flooring - epoxy | 14 | 14 | 19-Feb-15 | 10-Mar-15 | 9 |
| SW-2040 | Zone 4 - Fine grade for sidewalk and planter curb | 3 | 3 | 19-Feb-15 | 23-Feb-15 | 17 |
| LL1-Z3-FCC38 | Final clean and punch list at FCC | 3 | 3 | 19-Feb-15 | 23-Feb-15 | 26 |
| LL1-Z2-8136 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 19-Feb-15 | 23-Feb-15 | 22 |
| I-3102 | GWB, tape & finish ceiling at East Ballroom | 7 | 7 | 19-Feb-15 | 27-Feb-15 | 0 |
| GB1117-114 | Complete plumbing fixture installation - Levels 3, 11-1 | 4 | 4 | 19-Feb-15 | 24-Feb-15 | 29 |
| MPP-1004 | (C) Pool Area cornice metal | 8 | 8 | 20-Feb-15 | 28-Feb-15 | 12 |

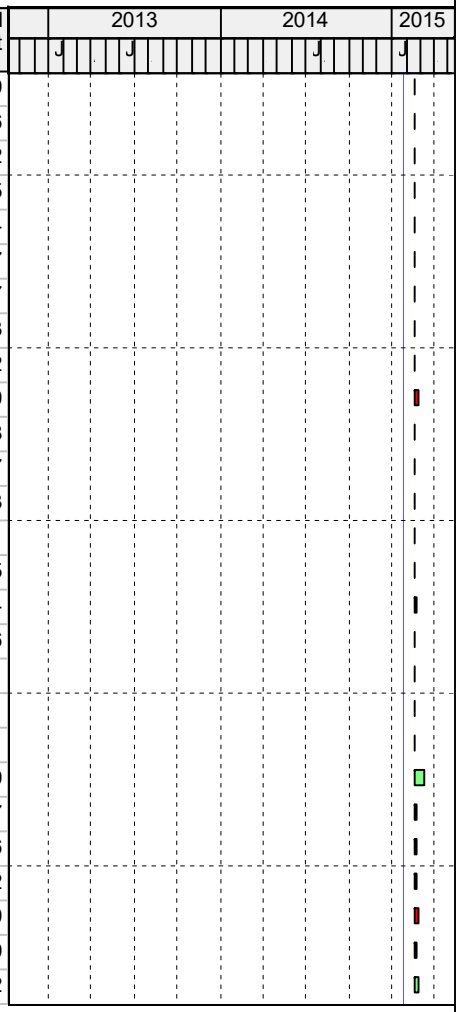



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8648 | Install pool topping slab | 2 | 2 | 20-Feb-15 | 23-Feb-15 | 2 |
| CO-7402 | Cx - FPT - Central Plant | 2 | 2 | 20-Feb-15 | 23-Feb-15 | 42 |
| SW-2044 | Zone 4 - FRP sidewalk | 5 | 5 | 20-Feb-15 | 26-Feb-15 | 17 |
| LL1-8152 | Complete MEP trim | 2 | 2 | 20-Feb-15 | 23-Feb-15 | 29 |
| LL1-Z2-8160 | Flooring - carpet | 5 | 5 | 20-Feb-15 | 26-Feb-15 | 13 |
| L1K-8202 | Ceiling grid at Janitorial | 1 | 1 | 20-Feb-15 | 20-Feb-15 | 8 |
| LL1-8170 | Flooring - tile at elevator lobby | 3 | 3 | 20-Feb-15 | 24-Feb-15 | 25 |
| L1B-8148 | Lighting & electrical trim at corridors | 2 | 2 | 20-Feb-15 | 23-Feb-15 | 13 |
| L1B-8150 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 20-Feb-15 | 23-Feb-15 | 15 |
| L02-8172 | Finish carpentry/millwork at north half | 3 | 3 | 20-Feb-15 | 24-Feb-15 | 27 |
| L1BOH2C-6024 | Lighting & electrical trim at ceiling | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 16 |
| MPT-1052 | (A) Elevation 48/49 (north elevation, east of 51, L3-L | 3 | 3 | 23-Feb-15 | 25-Feb-15 | 37 |
| MPP-1024 | (B) Complete Elevation 4 (south elevation, east of tov | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 34 |
| MPT-1062 | (A) Elevation 32 metal panels (south elevation, east c | 8 | 8 | 23-Feb-15 | 03-Mar-15 | 12 |
| MPT-1064 | (B) Elevation 33/34 metal panels (east elevation, sou | 8 | 8 | 23-Feb-15 | 03-Mar-15 | 19 |
| LL1-8142 | Plumbing fixtures & trim | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 26 |
| LL1-8144 | Finish carpentry/millwork | 5 | 5 | 23-Feb-15 | 27-Feb-15 | 23 |
| L1L-8238 | HVAC drops/trim at celing | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 5 |
| L1L-8239 | Floor prep | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 9 |
| L1B-6019 | Install clouds at West Ballrooms | 7 | 7 | 23-Feb-15 | 03-Mar-15 | 3 |
| L1BOH2C-6026 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 16 |
| L1L-8142 | HVAC drops to 9-wood ceiling - north of Grid K | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 0 |
| L1L-8144 | Electrical drops to 9-wood ceiling - north of Grid K | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 0 |
| L1L-8146 | Fire sprinkler drops to 9-wood ceiling - north of Grid K | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 0 |
| GB1117-118 | Complete barn doors - Levels 3, 11-17 | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 31 |
| I-5138 | Bar plumbing relocation - paint | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 10 |
| L1L-8148 | Electrical rough-in at die wall | 5 | 5 | 23-Feb-15 | 27-Feb-15 | 9 |

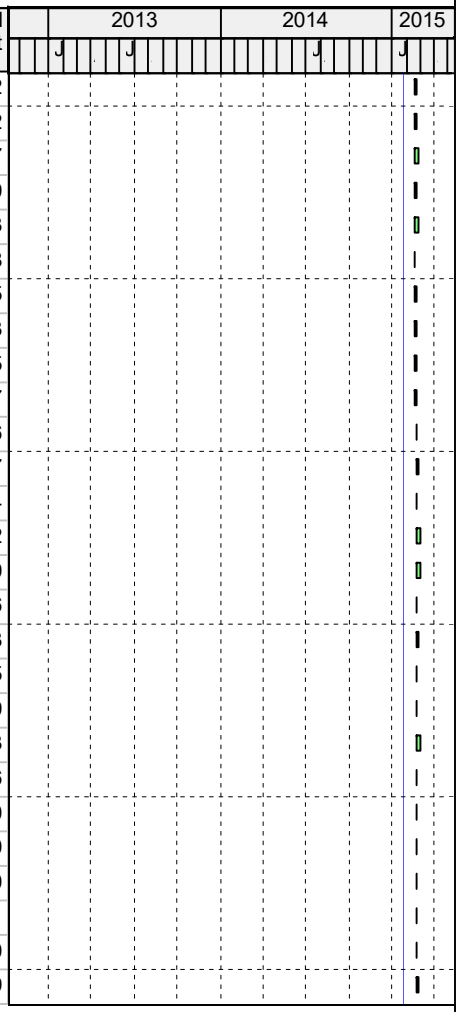



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8150 | Plumbing rough-in at die wall | 5 | 5 | 23-Feb-15 | 27-Feb-15 | 9 |
| L1L-8114a | Install 9-wood celing supports - south of Grid K | 3 | 3 | 23-Feb-15 | 25-Feb-15 | 2 |
| L1BOH2-8116 | Finish carpentry/millwork | 5 | 5 | 24-Feb-15 | 02-Mar-15 | 16 |
| L03-8612 | GWB hang, tape & finish walls at pool side rooms | 6 | 6 | 24-Feb-15 | 03-Mar-15 | 2 |
| LL2-2086 | Flooring - epoxy remainder of floor | 7 | 7 | 24-Feb-15 | 04-Mar-15 | 18 |
| CO-7408 | Cx - FPT - Garage Exhaust Fans | 1 | 1 | 24-Feb-15 | 24-Feb-15 | 42 |
| LL1-Z3-FCC40 | Install Knox Box at FCC | 2 | 2 | 24-Feb-15 | 25-Feb-15 | 26 |
| L1BOH2-8120 | Wall coverings - vinyl | 3 | 3 | 24-Feb-15 | 26-Feb-15 | 14 |
| LL1-Z2-8146 | Floor prep at corridors | 2 | 2 | 24-Feb-15 | 25-Feb-15 | 22 |
| L1K-8212 | Lighting & electrical trim at ceiling | 2 | 2 | 24-Feb-15 | 25-Feb-15 | 8 |
| L1B-8152 | Fire sprinkler drops/trim at corridors | 1 | 1 | 24-Feb-15 | 24-Feb-15 | 15 |
| L1B-8160 | Floor prep | 2 | 2 | 24-Feb-15 | 25-Feb-15 | 13 |
| L1BOH2-8112 | Fire sprinkler drops/trim at ceiling | 1 | 1 | 25-Feb-15 | 25-Feb-15 | 17 |
| MPP-1012 | Caulking - Elevation 4 (south elevation, east of tower) | 6 | 6 | 25-Feb-15 | 04-Mar-15 | 30 |
| CO-7410 | Cx - FPT - Misc Equipment | 4 | 4 | 25-Feb-15 | 02-Mar-15 | 42 |
| LL1-8150 | Install bathroom accessories | 2 | 2 | 25-Feb-15 | 26-Feb-15 | 26 |
| L1L-8236 | Lighting & electrical trim at ceilings | 3 | 3 | 25-Feb-15 | 27-Feb-15 | 5 |
| L1L-8286 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 25-Feb-15 | 27-Feb-15 | 5 |
| L1L-8302 | Lighting & electrical trim at ceilings | 3 | 3 | 25-Feb-15 | 27-Feb-15 | 5 |
| L1L-8304 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 25-Feb-15 | 27-Feb-15 | 5 |
| GB1117-116 | Complete shower doors - Levels 3, 11-17 | 2 | 2 | 25-Feb-15 | 26-Feb-15 | 29 |
| MPP-1058 | (B) Install podium cornice, south/east | 2 | 2 | 25-Feb-15 | 26-Feb-15 | 34 |
| SW-2066 | Porte Cochere - FRP planter curb | 2 | 2 | 25-Feb-15 | 26-Feb-15 | 17 |
| LL1-Z3-FCC22 | Final inspections by CoB and Fire Marshall | 2 | 2 | 26-Feb-15 | 27-Feb-15 | 26 |
| MPT-1082 | Caulking - Elevation 48/49 (north elevation, east of 5 | 4 | 4 | 26-Feb-15 | 03-Mar-15 | 31 |
| L1B-8130 | Flooring - VCT at service corridor and A/V room | 3 | 3 | 26-Feb-15 | 02-Mar-15 | 14 |
| L1K-8218 | Floor prep | 2 | 2 | 26-Feb-15 | 27-Feb-15 | 8 |

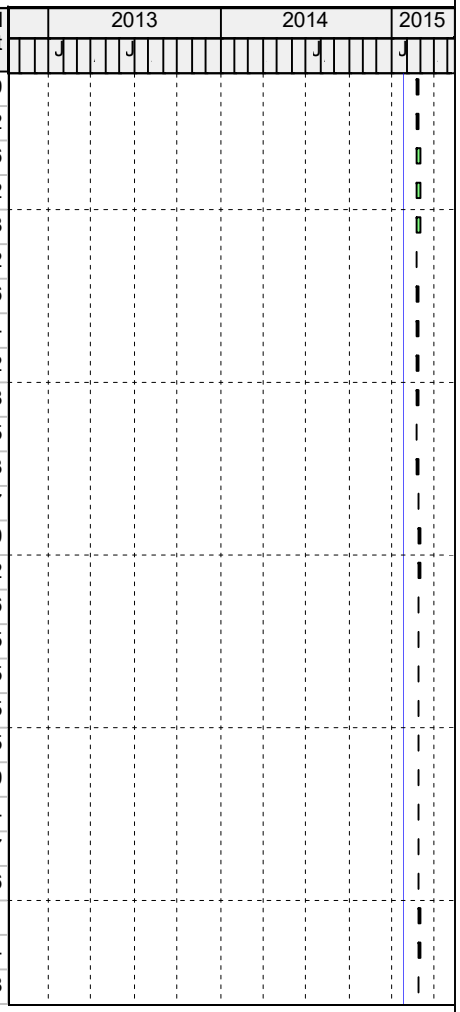



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-8154 | Finish carpentry/millwork at corridors | 10 | 10 | 26-Feb-15 | 11-Mar-15 | 13 |
| L1L-8142a | HVAC drops to 9-wood ceiling - south of Grid K | 2 | 2 | 26-Feb-15 | 27-Feb-15 | 2 |
| L1L-8144a | Electrical drops to 9-wood ceiling - south of Grid K | 2 | 2 | 26-Feb-15 | 27-Feb-15 | 2 |
| L1L-8146a | Fire sprinkler drops to 9-wood ceiling - south of Grid K | 2 | 2 | 26-Feb-15 | 27-Feb-15 | 2 |
| CO-7428 | Cx - Pressure Testing - GC Indicates Podium Complet | 0 | 0 | | 26-Feb-15 | 31 |
| LL1-Z2-8152 | Complete MEP trim | 2 | 2 | 27-Feb-15 | 02-Mar-15 | 24 |
| I-1208 | Paint, prime & first coat finish | 2 | 2 | 27-Feb-15 | 02-Mar-15 | 0 |
| L1BOH2-8123 | Floor prep | 2 | 2 | 27-Feb-15 | 02-Mar-15 | 14 |
| SW-2056 | Zone 4 - Pull wire and replace luminaires on 110th | 5 | 5 | 27-Feb-15 | 05-Mar-15 | 27 |
| LL1-8162 | Flooring - carpet at corridors | 5 | 5 | 27-Feb-15 | 05-Mar-15 | 13 |
| LL1-Z2-8148 | Flooring - carpet at corridors | 3 | 3 | 27-Feb-15 | 03-Mar-15 | 21 |
| LL1-Z2-8150 | Install base at corridors | 3 | 3 | 27-Feb-15 | 03-Mar-15 | 21 |
| MPP-1060 | (B) Install alcoves, south | 2 | 2 | 27-Feb-15 | 28-Feb-15 | 39 |
| SW-2062 | Zone 4 - Patch curb & gutter | 2 | 2 | 27-Feb-15 | 02-Mar-15 | 20 |
| SW-2064 | Porte Cochere - Fill and grade Porte Cochere drive | 3 | 3 | 27-Feb-15 | 03-Mar-15 | 17 |
| MPT-1108 | Cap metal - complete at tower | 5 | 5 | 27-Feb-15 | 05-Mar-15 | 29 |
| MPT-1112 | Cap metal - complete at Ballroom roof | 3 | 3 | 27-Feb-15 | 03-Mar-15 | 28 |
| CO-7430 | Cx - Pressure Testing - Pre-Walk with GC (Tower) | 1 | 1 | 27-Feb-15 | 27-Feb-15 | 31 |
| L1K-8210 | Ceramic tile in restrooms | 7 | 7 | 02-Mar-15 | 10-Mar-15 | 8 |
| MPP-1040 | Caulking - Pool Area & Ballroom cornice metal | 8 | 8 | 02-Mar-15 | 11-Mar-15 | 10 |
| LL1-8146 | Complete MEP trim | 2 | 2 | 02-Mar-15 | 03-Mar-15 | 23 |
| LL1-8148 | Acoustical ceiling tile | 2 | 2 | 02-Mar-15 | 03-Mar-15 | 23 |
| L1L-8234 | Fire sprinkler trim at ceilings | 1 | 1 | 02-Mar-15 | 02-Mar-15 | 5 |
| LL2-8106b | Pinned insulation at ramp at Garage | 3 | 3 | 02-Mar-15 | 04-Mar-15 | 23 |
| LL1-8188 | Paint, final coat & touch-up | 2 | 2 | 02-Mar-15 | 03-Mar-15 | 23 |
| L1B-6037 | Install clouds at East Ballroom | 7 | 7 | 02-Mar-15 | 10-Mar-15 | 0 |
| L1L-8306 | Fire sprinkler trim | 1 | 1 | 02-Mar-15 | 02-Mar-15 | 5 |

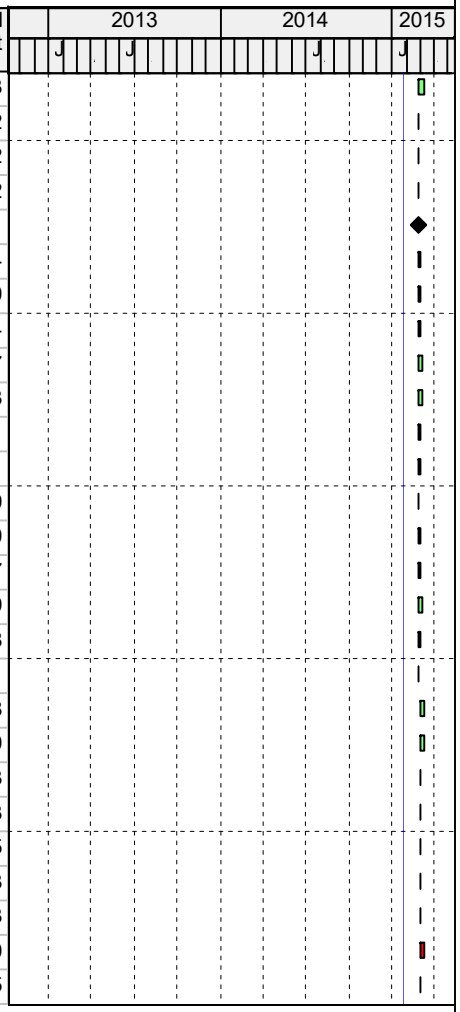



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8308 | Floor (stair) prep | 1 | 1 | 02-Mar-15 | 02-Mar-15 | 5 |
| L1L-8152 | Install bar ceiling | 5 | 5 | 02-Mar-15 | 06-Mar-15 | 9 |
| CO-7432 | Cx - Pressure Testing - GC Makes Corrections (Tower) | 5 | 5 | 02-Mar-15 | 06-Mar-15 | 31 |
| L1BOH2-8124 | Flooring - VCT | 3 | 3 | 03-Mar-15 | 05-Mar-15 | 14 |
| L1BOH2-8124a | Install base | 5 | 5 | 03-Mar-15 | 09-Mar-15 | 16 |
| I-1206 | Install ceiling at Concierge Lounge | 10 | 10 | 03-Mar-15 | 16-Mar-15 | 0 |
| SW-2042 | Porte Cochere - Install trench drain | 3 | 3 | 03-Mar-15 | 05-Mar-15 | 17 |
| L1L-8242 | Finish carpentry/millwork (including front desk) | 15 | 15 | 03-Mar-15 | 23-Mar-15 | 5 |
| L1L-8260 | Wall coverings - vinyl | 3 | 3 | 03-Mar-15 | 05-Mar-15 | 9 |
| L1L-8280 | Install Peter Glassford art wall | 5 | 5 | 03-Mar-15 | 09-Mar-15 | 5 |
| L03-8614 | Paint & wall finishes at Pool | 3 | 3 | 04-Mar-15 | 06-Mar-15 | 2 |
| L03-8630 | Install doors & hardware at Pool | 2 | 2 | 04-Mar-15 | 05-Mar-15 | 6 |
| MPT-1094 | Caulking - Elevation 32 (south elevation, east of man | 10 | 10 | 04-Mar-15 | 17-Mar-15 | 16 |
| MPT-1096 | Caulking - Elevation 33/34 (east elevation, south end | 10 | 10 | 04-Mar-15 | 17-Mar-15 | 16 |
| LL1-Z2-8154 | Complete MEP trim in corridors | 2 | 2 | 04-Mar-15 | 05-Mar-15 | 21 |
| MPT-1100 | (B) Install spandrel, east (Elevation 44) | 2 | 2 | 04-Mar-15 | 05-Mar-15 | 12 |
| MPT-1102 | (A) Elevation 32 spandrel panels (south elevation, ea | 2 | 2 | 04-Mar-15 | 05-Mar-15 | 12 |
| MPT-1116 | Cap metal - Pool high roof | 3 | 3 | 04-Mar-15 | 06-Mar-15 | 28 |
| L1L-8140a | Install 9-wood ceiling - south of Grid K | 5 | 5 | 04-Mar-15 | 10-Mar-15 | 0 |
| LL2-2048 | Set Laundry Room equipment (BY OTHERS) | 2 | 2 | 05-Mar-15 | 06-Mar-15 | 18 |
| L02-8138 | Acoustical ceiling tile at south half | 2 | 2 | 05-Mar-15 | 06-Mar-15 | 21 |
| CO-7406 | Cx - FPT - MUA, RTU, VAV and Exhaust Fans | 5 | 5 | 05-Mar-15 | 11-Mar-15 | 28 |
| MPP-1036 | Podium Signs, East | 5 | 5 | 05-Mar-15 | 11-Mar-15 | 20 |
| L1L-8206 | Lighting & electrical trim at ceilings - north of Grid K | 2 | 2 | 05-Mar-15 | 06-Mar-15 | 8 |
| L02-8174 | Complete MEP trim at north half | 2 | 2 | 05-Mar-15 | 06-Mar-15 | 21 |
| L02-8176 | Paint, final coat & touch-up at north half | 2 | 2 | 05-Mar-15 | 06-Mar-15 | 21 |
| L02-8180 | Acoustical ceiling tile at north half | 2 | 2 | 05-Mar-15 | 06-Mar-15 | 21 |

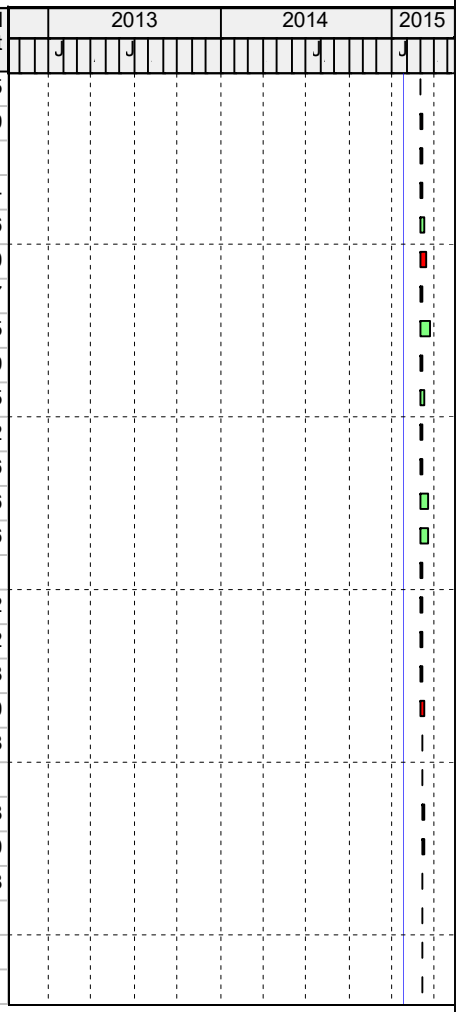



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8640 | Prep and install pool plaster | 3 | 3 | 06-Mar-15 | 10-Mar-15 | 2 |
| SW-2048 | Porte Cochere - FRP Porte Cochere drive | 10 | 10 | 06-Mar-15 | 19-Mar-15 | 17 |
| L1L-8123 | Floor prep - north of Grid K | 2 | 2 | 06-Mar-15 | 09-Mar-15 | 8 |
| LL1-8166 | Install base at corridors | 5 | 5 | 06-Mar-15 | 12-Mar-15 | 13 |
| LL1-Z3-8128 | Flooring - VCT | 3 | 3 | 06-Mar-15 | 10-Mar-15 | 14 |
| CO-7144 | Final Inspection - Transportation (Right-Of-Way) | 5 | 5 | 06-Mar-15 | 12-Mar-15 | 34 |
| CO-7148 | Final Inspection - Utilities | 5 | 5 | 06-Mar-15 | 12-Mar-15 | 34 |
| LL2-2050 | Laundry Room equipment final connections (MEP) | 1 | 1 | 09-Mar-15 | 09-Mar-15 | 18 |
| LL2-2090 | Acoustical ceiling tile at Laundry | 2 | 2 | 09-Mar-15 | 10-Mar-15 | 18 |
| LL2-2092 | Complete MEP trim at Laundry | 2 | 2 | 09-Mar-15 | 10-Mar-15 | 18 |
| LL2-8144 | Acoustical ceiling tile | 3 | 3 | 09-Mar-15 | 11-Mar-15 | 18 |
| L1B-8206 | Ceiling grid at West Ballrooms | 4 | 4 | 09-Mar-15 | 12-Mar-15 | 3 |
| CO-7154 | Final Inspection - Mechanical | 5 | 5 | 09-Mar-15 | 13-Mar-15 | 33 |
| CO-7434 | Cx - Pressure Testing - Pressure Pre-Test (Tower) | 2 | 2 | 09-Mar-15 | 10-Mar-15 | 31 |
| L1BOH2-8128 | Flooring - carpet | 3 | 3 | 10-Mar-15 | 12-Mar-15 | 16 |
| L1L-8266 | HVAC drops/trim at celing | 2 | 2 | 10-Mar-15 | 11-Mar-15 | 1 |
| L1L-8278 | Flooring - tile at stair treads | 10 | 10 | 10-Mar-15 | 23-Mar-15 | 5 |
| L1K-8128 | Install Kitchen equipment (BY OTHERS) | 5 | 5 | 11-Mar-15 | 17-Mar-15 | 9 |
| L03-8642 | Fill pool | 1 | 1 | 11-Mar-15 | 11-Mar-15 | 2 |
| LL1-Z3-8152 | Complete MEP trim | 2 | 2 | 11-Mar-15 | 12-Mar-15 | 17 |
| L1K-8220 | Install countertops in restrooms | 2 | 2 | 11-Mar-15 | 12-Mar-15 | 10 |
| L1K-8222 | Install toilet partitions | 4 | 4 | 11-Mar-15 | 16-Mar-15 | 8 |
| L1L-8204a | HVAC trim at ceiling - south of Grid K | 1 | 1 | 11-Mar-15 | 11-Mar-15 | 0 |
| CO-7436 | Cx - Pressure Testing -Corrections (Tower) | 2 | 2 | 11-Mar-15 | 12-Mar-15 | 31 |
| L03-8644 | Connect, startup & adjust pool equipment | 10 | 10 | 12-Mar-15 | 25-Mar-15 | 14 |
| SW-2218 | Zone 2 - Install landscaping & irrigation | 5 | 5 | 12-Mar-15 | 18-Mar-15 | 10 |
| RF-4066 | Pool Green Roof - Install decorative metal railing | 3 | 3 | 12-Mar-15 | 16-Mar-15 | 19 |

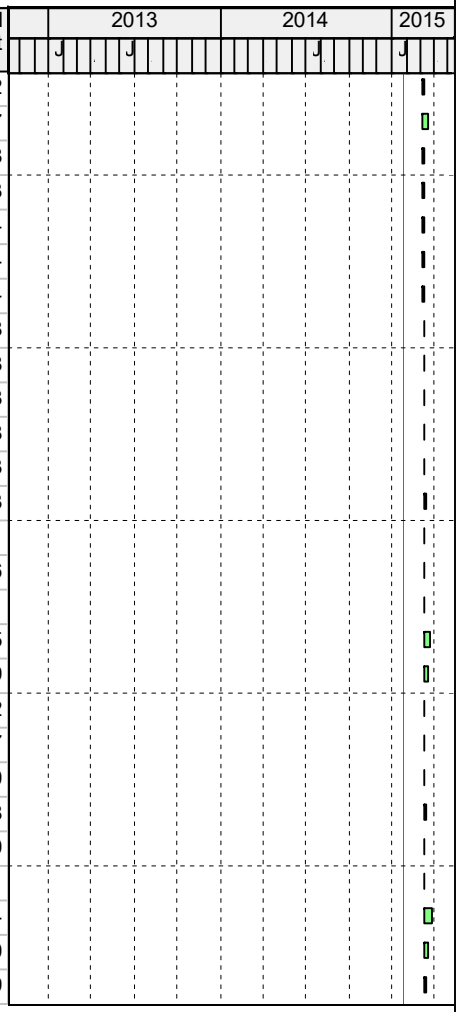



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8264 | Lighting & electrical trim at ceilings | 2 | 2 | 12-Mar-15 | 13-Mar-15 | 1 |
| L1B-8156 | Install base at corridors | 5 | 5 | 12-Mar-15 | 18-Mar-15 | 13 |
| L1L-8298 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 12-Mar-15 | 13-Mar-15 | 2 |
| CN-1000 | Install exterior canopies - steel | 5 | 5 | 12-Mar-15 | 18-Mar-15 | 15 |
| L1L-8206a | Lighting & elecrical trim at ceilings - south of Grid K | 2 | 2 | 12-Mar-15 | 13-Mar-15 | 0 |
| L1BOH2-8140 | Acoustical ceiling tile | 2 | 2 | 13-Mar-15 | 16-Mar-15 | 16 |
| L1BOH2-8201 | Paint, final coat & touch-up | 2 | 2 | 13-Mar-15 | 16-Mar-15 | 16 |
| L1BOH2-8118 | Complete MEP trim | 2 | 2 | 13-Mar-15 | 16-Mar-15 | 16 |
| LL1-8164 | Complete MEP trim at corridors | 2 | 2 | 13-Mar-15 | 16-Mar-15 | 14 |
| LL1-8168 | Paint, final coat & touch-up | 2 | 2 | 13-Mar-15 | 16-Mar-15 | 14 |
| LL1-Z2-8156 | Paint, final coat & touch-up | 2 | 2 | 13-Mar-15 | 16-Mar-15 | 14 |
| L1L-8123a | Floor prep - south of Grid K | 2 | 2 | 13-Mar-15 | 16-Mar-15 | 0 |
| L1B-8202 | Wall coverings - vinyl at Ballrooms | 5 | 5 | 16-Mar-15 | 20-Mar-15 | 4 |
| L1L-8262 | Fire sprinkler trim at ceilings | 1 | 1 | 16-Mar-15 | 16-Mar-15 | 2 |
| L1B-8208 | Ceiling grid at East Ballroom | 4 | 4 | 16-Mar-15 | 19-Mar-15 | 0 |
| L1L-8112a | Fire sprinkler trim - south of Grid K | 1 | 1 | 16-Mar-15 | 16-Mar-15 | 0 |
| L1L-8118a | Fire alarm trim (spreaker strobe & smoke detector bas | 1 | 1 | 16-Mar-15 | 16-Mar-15 | 0 |
| L1BOH2-8134 | Clean | 2 | 2 | 17-Mar-15 | 18-Mar-15 | 16 |
| CO-7110T | Fire Sprinkler Pre-Testing (Tower) - Tower Levels 4 thru | 6 | 6 | 17-Mar-15 | 24-Mar-15 | 2 |
| RF-4068 | Pool Green Roof - Install American Hydrotech assembl | 3 | 3 | 17-Mar-15 | 19-Mar-15 | 19 |
| L1K-8206 | Plumbing fixtures & trim at Restrooms | 5 | 5 | 17-Mar-15 | 23-Mar-15 | 8 |
| CO-7141 | Install remaining devices & prep devices for testing - I | 7 | 7 | 17-Mar-15 | 25-Mar-15 | 9 |
| L1L-8136 | Install Peter Glassford art wall | 10 | 10 | 17-Mar-15 | 30-Mar-15 | 8 |
| L1L-8138 | Flooring - epoxy floor at bar | 5 | 5 | 17-Mar-15 | 23-Mar-15 | 3 |
| I-1210 | Floor prep | 2 | 2 | 17-Mar-15 | 18-Mar-15 | 0 |
| L1L-8124b | Flooring - wood - south of Grid K | 5 | 5 | 17-Mar-15 | 23-Mar-15 | 0 |
| L1K-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 12 |

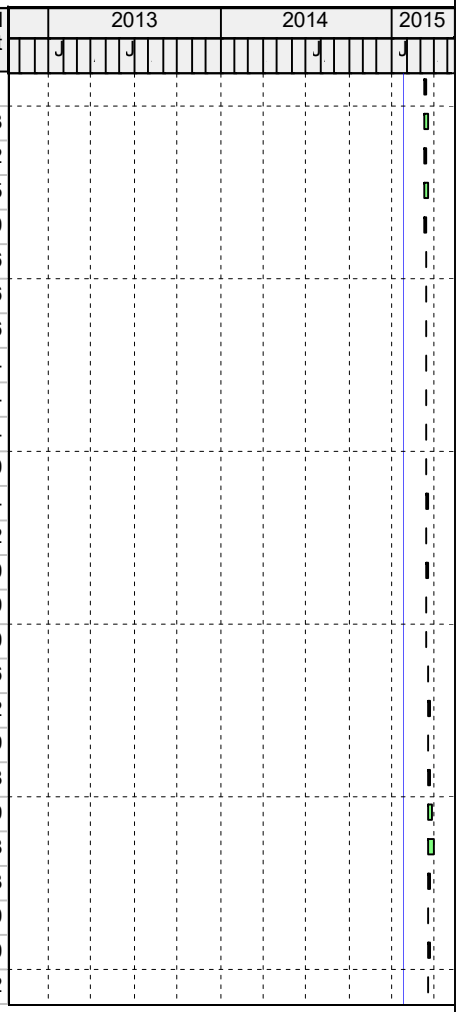



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8128a | Kitchen Equipment Final Connections | 5 | 5 | 18-Mar-15 | 24-Mar-15 | 9 |
| L1K-8142 | Complete MEP trim | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 12 |
| MPP-1038 | Podium Signs, West | 5 | 5 | 18-Mar-15 | 24-Mar-15 | 16 |
| MPT-1074 | Tower Sign, South (El 32) | 5 | 5 | 18-Mar-15 | 24-Mar-15 | 16 |
| L1K-8154 | Acoustical ceiling tile | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 12 |
| L1K-8156 | Complete MEP trim | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 12 |
| L1K-8158 | Paint, final coat & touch-up | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 12 |
| CO-7142 | Fire Alarm System Device Testing - Podium | 7 | 7 | 18-Mar-15 | 26-Mar-15 | 9 |
| L1BOH2-8132 | Punch | 4 | 4 | 19-Mar-15 | 24-Mar-15 | 16 |
| I-1202 | Flooring - tile & carpet at Concierge Lounge | 6 | 6 | 19-Mar-15 | 26-Mar-15 | 0 |
| L03-8618 | Ceramic tile at pool area | 5 | 5 | 19-Mar-15 | 25-Mar-15 | 2 |
| L03-8638 | Install pool deck and ADA lift | 3 | 3 | 19-Mar-15 | 23-Mar-15 | 4 |
| SW-2330 | Zone 3 - Landscaping & irrigation | 5 | 5 | 19-Mar-15 | 25-Mar-15 | 10 |
| L1B-8164 | Acoustical ceiling tile | 2 | 2 | 19-Mar-15 | 20-Mar-15 | 16 |
| L1B-8166 | Complete MEP trim | 2 | 2 | 19-Mar-15 | 20-Mar-15 | 16 |
| CN-1002 | Install exterior canopies - glass | 5 | 5 | 19-Mar-15 | 25-Mar-15 | 15 |
| LL2-8150 | LL2 Floor Complete | 0 | 0 | | 20-Mar-15 | 18 |
| CM-1016a | CM - Owner FF+E "Build-Out" - Floors 3, 11-17 | 21 | 21 | 23-Mar-15 | 13-Apr-15 | 17 |
| L1K-8208 | Install restroom accessories | 2 | 2 | 24-Mar-15 | 25-Mar-15 | 8 |
| L1L-8130 | Install bar and back bar | 10 | 10 | 24-Mar-15 | 06-Apr-15 | 3 |
| L1L-8240 | Flooring - tile & base | 10 | 10 | 24-Mar-15 | 06-Apr-15 | 5 |
| L1L-8244 | Complete MEP trim | 2 | 2 | 24-Mar-15 | 25-Mar-15 | 13 |
| L1L-8282 | Finish carpentry/millwork | 5 | 5 | 24-Mar-15 | 30-Mar-15 | 8 |
| L1K-8216 | Complete MEP trim | 2 | 2 | 24-Mar-15 | 25-Mar-15 | 8 |
| L1L-8288 | Paint, final coat & touch-up | 2 | 2 | 24-Mar-15 | 25-Mar-15 | 13 |
| L1L-8116a | Finish carpentry/millwork - south of Grid K | 10 | 10 | 24-Mar-15 | 06-Apr-15 | 0 |
| L1BOH2-81214 | L1, Zone 3 Complete | 0 | 0 | | 24-Mar-15 | 16 |

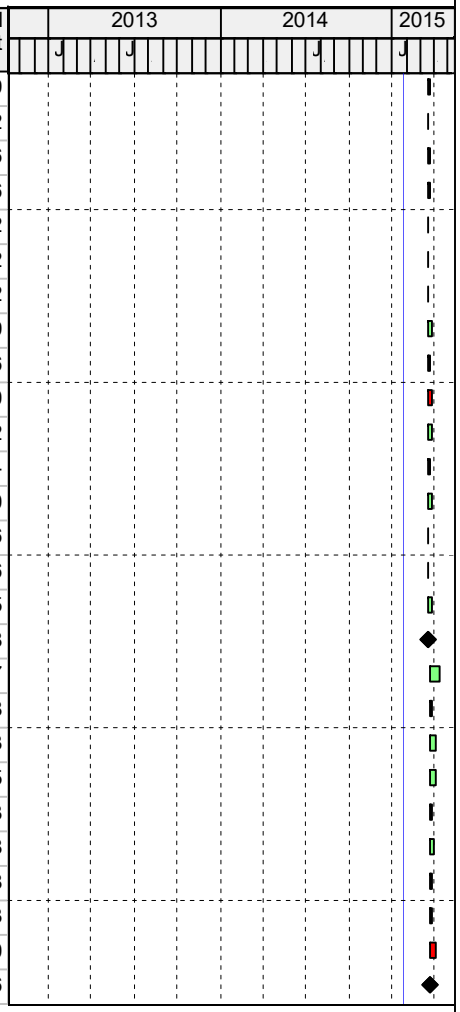



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7104T | Fire Alarm & Smoke Control Pre-Testing (Tower) - Tow | 7 | 7 | 25-Mar-15 | 02-Apr-15 | 8 |
| CO-7110T.1 | Fire Sprinkler Pre-Testing (Tower) - Tower Levels 3, 11 | 6 | 6 | 25-Mar-15 | 01-Apr-15 | 2 |
| L1B-8129 | Floor prep | 2 | 2 | 25-Mar-15 | 26-Mar-15 | 0 |
| CO-7156 | Final Inspection - Health Department (Kitchens) | 5 | 5 | 25-Mar-15 | 31-Mar-15 | 21 |
| L03-8620 | Plumbing fixtures & trim at Pool | 2 | 2 | 26-Mar-15 | 27-Mar-15 | 3 |
| L03-8626 | Electrical trim & finish at Pool | 2 | 2 | 26-Mar-15 | 27-Mar-15 | 3 |
| L03-8628 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 26-Mar-15 | 27-Mar-15 | 3 |
| SW-2122 | Zone 1 - Install landscaping & irrigation | 3 | 3 | 26-Mar-15 | 30-Mar-15 | 10 |
| L03-8674 | Install storfront at Pool entry | 2 | 2 | 26-Mar-15 | 27-Mar-15 | 2 |
| I-1204 | Finish carpentry/millwork at Concierge Lounge | 10 | 10 | 27-Mar-15 | 09-Apr-15 | 0 |
| L1B-8128 | Install base at Ballrooms | 5 | 5 | 27-Mar-15 | 02-Apr-15 | 0 |
| L1L-8284 | Install handrails | 2 | 2 | 27-Mar-15 | 30-Mar-15 | 8 |
| L03-8632 | Install restroom accessories at Pool | 2 | 2 | 30-Mar-15 | 31-Mar-15 | 3 |
| L03-8646 | Health inspection | 1 | 1 | 01-Apr-15 | 01-Apr-15 | 10 |
| L03-8218 | Install base at corridors | 1 | 1 | 01-Apr-15 | 01-Apr-15 | 2 |
| CO-7104T.1 | Fire Alarm & Smoke Control Pre-Testing (Tower) - Tow | 7 | 7 | 02-Apr-15 | 10-Apr-15 | 2 |
| L1L-8120 | Plumbing fixtures & trim at bar | 2 | 2 | 07-Apr-15 | 08-Apr-15 | 1 |
| L1L-8122 | Electrical trim & finish at bar | 2 | 2 | 07-Apr-15 | 08-Apr-15 | 1 |
| L1L-8124a | Install base | 3 | 3 | 07-Apr-15 | 09-Apr-15 | 0 |
| L1B-8158 | Flooring - carpet at corridors | 3 | 3 | 07-Apr-15 | 09-Apr-15 | 0 |
| L1L-8203 | Complete MEP trim | 2 | 2 | 07-Apr-15 | 08-Apr-15 | 3 |
| CO-7146 | Final Inspection - Clear & Grade | 5 | 5 | 09-Apr-15 | 15-Apr-15 | 10 |
| CO-7152 | Final Inspection - Plumbing | 5 | 5 | 09-Apr-15 | 15-Apr-15 | 10 |
| L1B-8136 | Complete MEP trim | 2 | 2 | 10-Apr-15 | 13-Apr-15 | 0 |
| L1L-8268 | Complete MEP trim | 2 | 2 | 10-Apr-15 | 13-Apr-15 | 0 |
| L1B-8168 | Paint, final coat & touch-up | 2 | 2 | 10-Apr-15 | 13-Apr-15 | 0 |
| L1L-8300 | Paint, final coat & touch-up | 2 | 2 | 10-Apr-15 | 13-Apr-15 | 0 |

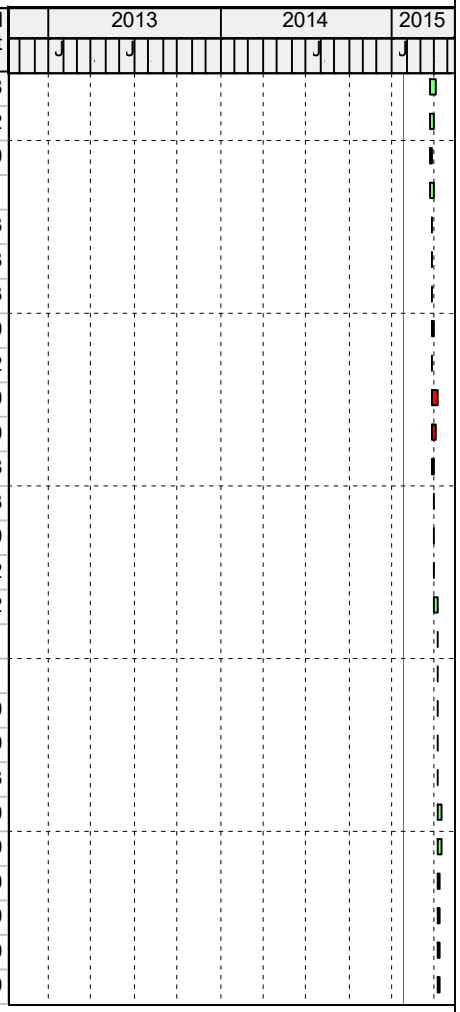



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7500 | Complete Final Walsh/WPM Inspections/Corrections | 10 | 10 | 10-Apr-15 | 23-Apr-15 | 4 |
| CO-7112T | City of Bellevue/3rd Party Fire Sprinkler Inspection / A | 6 | 6 | 13-Apr-15 | 20-Apr-15 | 2 |
| CO-7118T | City of Bellevue/3rd Party Fire Alarm Inspection / Appl | 6 | 6 | 13-Apr-15 | 20-Apr-15 | 2 |
| CO-7106T | City of Bellevue/3rd Party Smoke Control Testing (Tow | 6 | 6 | 13-Apr-15 | 20-Apr-15 | 2 |
| CO-7150 | Final Inspection - Electrical | 5 | 5 | 14-Apr-15 | 20-Apr-15 | 7 |
| CO-7412 | Cx - Pressure Testing - GC Indicates Podium Complet | 0 | 0 | | 14-Apr-15 | 0 |
| CO-7416 | Cx - Pressure Testing - Pre-Walk with GC (Podium) | 1 | 1 | 14-Apr-15 | 15-Apr-15 | 0 |
| CO-7418 | Cx - Pressure Testing - GC Makes Corrections (Podiu | 5 | 5 | 14-Apr-15 | 21-Apr-15 | 0 |
| CO-7420 | Cx - Pressure Testing - Pressure Pre-Test (Podium) | 2 | 2 | 21-Apr-15 | 23-Apr-15 | 0 |
| CM-1022 | Podium - "Clean/Punch" Complete - All Floors, All Zon | 0 | 0 | | 22-Apr-15 | 10 |
| CO-7422 | Cx - Pressure Testing -Corrections (Podium) | 2 | 2 | 23-Apr-15 | 27-Apr-15 | 0 |
| CO-7424 | Cx - Pressure Testing - Pressure Final Test | 1 | 1 | 27-Apr-15 | 28-Apr-15 | 0 |
| CO-7426 | Cx - Pressure Testing - Building Final Corrections | 2 | 2 | 28-Apr-15 | 30-Apr-15 | 0 |
| CO-7124 | Final Inspection - Building Department | 5 | 5 | 30-Apr-15 | 07-May-15 | 0 |
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13 A | | |
| CM-1002 | CM - Contract Time (578 Cal Days) | 576 | 0 | 06-Mar-13 A | 05-Oct-14 A | |
| CM-1014 | CM - Start of Construction | 0 | 0 | 05-Apr-13 A | | |
| CM-1006 | Construction Documents Issued by Client - (Due on 7 | 0 | 0 | 26-Jan-15 | | 101 |
| CM-1008 | Finalization of Allowances - (Due on 9-2-13) | 0 | 0 | 26-Jan-15 | | 101 |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 02-Mar-15* | | 13 |
| CM-1016 | CM - Owner FF+E "Build-Out" - Floors 4-10 | 21 | 21 | 02-Mar-15 | 23-Mar-15 | 17 |
| CO-7004 | CO - Prep / Submit O&M Manuals | 30 | 30 | 21-Mar-15 | 20-Apr-15 | 17 |
| CM-1018 | CM - Hotel Operations Training | 21 | 21 | 30-Mar-15 | 20-Apr-15 | 17 |
| CO-7006 | CO - Certificate of Occupancy/Substantial Completior | 0 | 0 | | 07-May-15 | 0 |

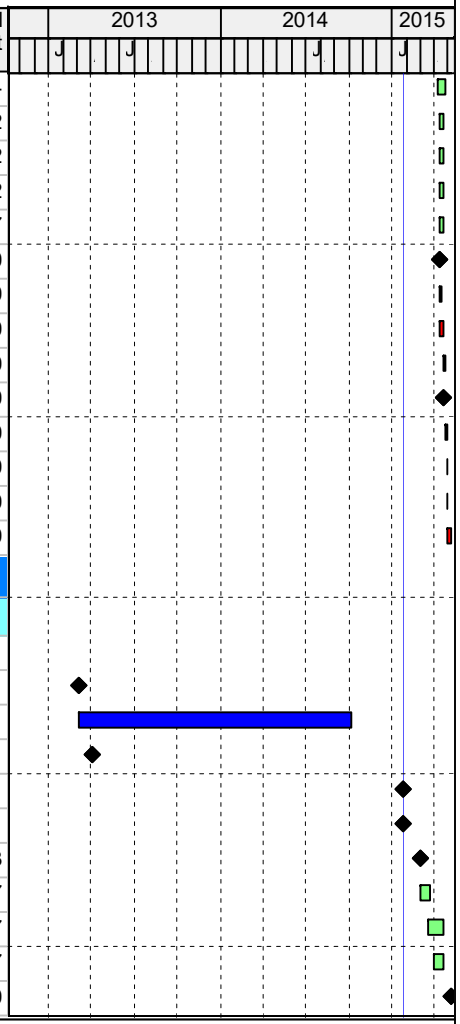


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7122 | CO - Certificate of Occupancy | 0 | 0 | | 07-May-15 | 0 |
| **Misc Milestones** | | | | | | |
| CM-1020 | MM - Site Mobilization | 10 | 0 | 06-Mar-13 A | 04-Apr-13 A | |
| MM-1008 | MM - Top Out - Tower / Structure | 0 | 0 | | 16-Apr-14 A | |
| MM-1004 | MM - Start Drywall In Tower | 0 | 0 | 27-Jun-14 A | | |
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 06-Sep-14 A | |
| MM-1010 | Energize Permanent Power | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| **Tower Crane** | | | | | | |
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 0 | 04-Jun-13 A | 14-Jun-13 A | |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 0 | 20-Jun-13 A | 24-Jun-13 A | |
| TC-5902 | Tower Crane - Erectiion | 2 | 0 | 21-Jun-13 A | 24-Jun-13 A | |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 24-Jun-13 A | | |
| TC-5906 | Tower Crane - Operatational Period | 391 | 0 | 24-Jun-13 A | 16-Jun-14 A | |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 0 | 16-Jun-14 A | 17-Jun-14 A | |
| **Man & Material Lifts** | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 0 | 14-Jan-14 A | 20-Jan-14 A | |
| ML-5952 | Man/Material Lifts - Erect/Build Loading Dock | 5 | 0 | 21-Jan-14 A | 27-Jan-14 A | |
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 10-Feb-14 A | | |
| ML-5954 | Man/Material Lifts - Load Test / Certify | 1 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| ML-5958 | Man/Material Lifts - Operatational Period | 196 | 0 | 10-Feb-14 A | 15-Nov-14 A | |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 2 | 0 | 15-Nov-14 A | 16-Nov-14 A | |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |
| **Mass Excavation / Shoring** | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 0 | 05-Apr-13 A | 12-Apr-13 A | |

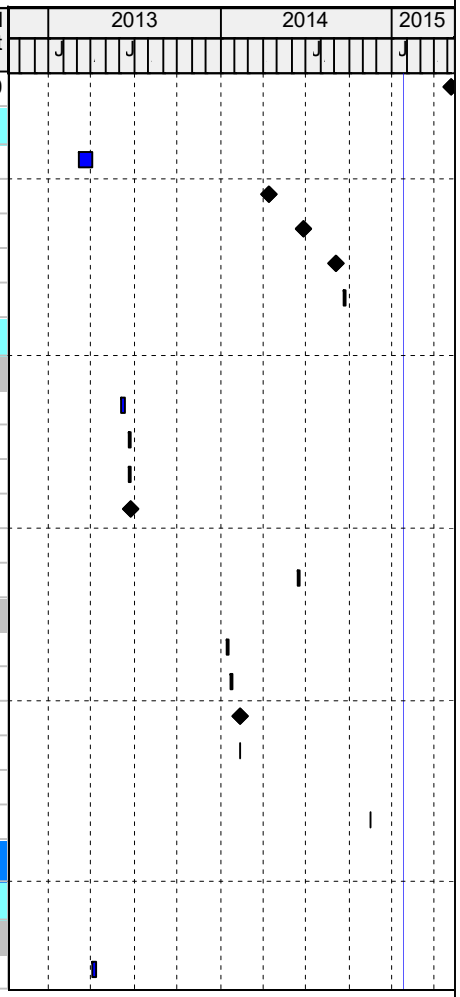



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2002 | Demolition And Utility Relocation | 8 | 0 | 15-Apr-13 A | 19-Apr-13 A | |
| SW-2010 | Grade Subgrade for Elect/Plumbing | 3 | 0 | 07-Jan-14 A | 09-Jan-14 A | |
| **Site Finishes** | | | | | | |
| SW-2006 | Install Perm Power Electrical Service / Dry Utilities (Ofl | 15 | 0 | 20-May-14 A | 05-Jun-14 A | |
| SW-2004 | Offsite Water & Water Connection | 9 | 0 | 22-Sep-14 A | 01-Oct-14 A | |
| SW-2008 | Zone 4 - Landscaping & irrigation | 7 | 7 | 31-Mar-15 | 08-Apr-15 | 10 |
| **Structure** | | | | | | |
| **Foundation / Substructure - (Levels LL4 / LL3)** | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 0 | 12-Jun-13 A | 27-Jun-13 A | |
| LL4-1601 | LL4 - Excavate Footings | 14 | 0 | 17-Jun-13 A | 30-Jul-13 A | |
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 0 | 18-Jun-13 A | 24-Jun-13 A | |
| LL4-1606 | LL4 - Undrgmd Plumbing | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-1608 | LL4 - Undrgmd Elec | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 0 | 19-Jun-13 A | 25-Jun-13 A | |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 0 | 26-Jun-13 A | 02-Aug-13 A | |
| LL4-2033 | LL4 - Shotcrete Walls | 27 | 0 | 26-Jun-13 A | 05-Aug-13 A | |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 0 | 03-Jul-13 A | 21-Aug-13 A | |
| LL4-1614 | LL4 - FRP SOG | 5 | 0 | 10-Jul-13 A | 07-Aug-13 A | |
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 0 | 12-Jul-13 A | 26-Jul-13 A | |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 0 | 13-Jul-13 A | 06-Aug-13 A | |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 0 | 22-Jul-13 A | 24-Jul-13 A | |
| LL4-1618 | LL4 - FRP Ramp SOG | 5 | 0 | 01-Aug-13 A | 07-Aug-13 A | |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2004 | LL2 - Shore / Form Deck | 8 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2006 | LL3 - M & E Inserts | 4 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2008 | LL3 - ReSteel / PT Cables | 6 | 0 | 05-Aug-13 A | 09-Aug-13 A | |

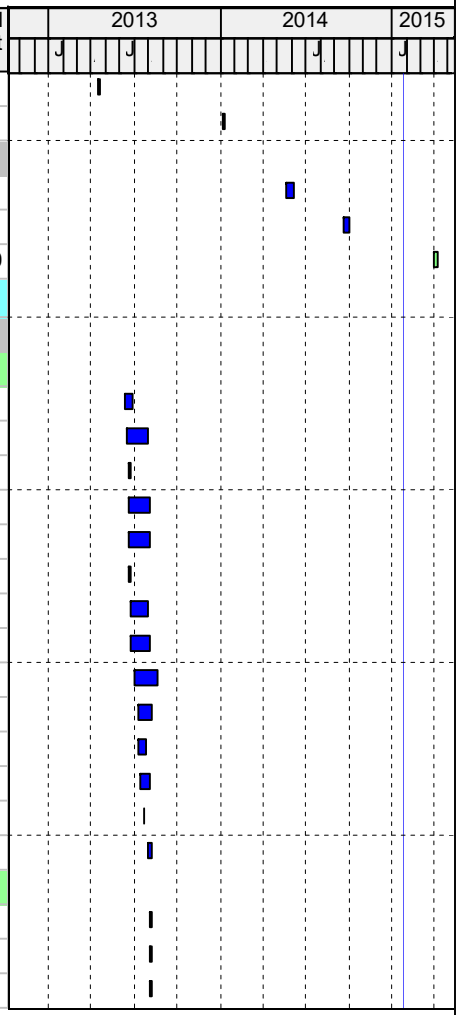


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-2010 | LL3 - Install Embeds | 2 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2001 | LL3 - Waterproof Walls | 3 | 0 | 05-Aug-13 A | 05-Aug-13 A | |
| LL3-2012 | LL3 - Pour / Finish Deck | 2 | 0 | 16-Aug-13 A | 16-Aug-13 A | |
| LL3-2014 | LL3 - Stress Tendons | 1 | 0 | 19-Aug-13 A | 19-Aug-13 A | |
| LL3-2000 | LL3 - FRP Core Walls | 8 | 0 | 19-Aug-13 A | 28-Aug-13 A | |
| LL3-2033 | LL3 - Shotcrete Walls | 5 | 0 | 23-Aug-13 A | 26-Aug-13 A | |
| LL3-2016 | LL3 - Strip / ReShore Deck | 3 | 0 | 01-Sep-13 A | 13-Sep-13 A | |
| LL3-2018 | LL3 - Remove ReShores | 4 | 0 | 04-Nov-13 A | 07-Nov-13 A | |
| Lower Podium - (Levels LL2 / LL1 / 1 / 2) | | | | | | |
| Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock) | | | | | | |
| Grids 1 to 4 - (SOG @ Loading Dock) | | | | | | |
| LL2-2056 | LL2 - Grease Intercepter | 5 | 0 | 15-Aug-13 A | 21-Aug-13 A | |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 0 | 27-Aug-13 A | 04-Sep-13 A | |
| LL2-2027 | LL2 - Waterproof Walls | 2 | 0 | 27-Aug-13 A | 28-Aug-13 A | |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 0 | 30-Aug-13 A | 05-Sep-13 A | |
| LL2-2021 | LL2 - FRP Elec Vault | 14 | 0 | 30-Aug-13 A | 04-Sep-13 A | |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 0 | 04-Sep-13 A | 11-Sep-13 A | |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 0 | 11-Sep-13 A | 13-Sep-13 A | |
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls/Roof | 11 | 0 | 19-Sep-13 A | 03-Oct-13 A | |
| LL2-2020 | LL2 - Undrgmd Plumbing | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2022 | LL2 - Undrgmd Elec | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2031 | LL2 - FRP Generator SOG | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2015 | LL2 to LL1 FRP Columns / Misc Walls | 6 | 0 | 01-Oct-13 A | 01-Oct-13 A | |
| LL2-2029 | LL2 - F/R/P Pour #2 | 8 | 0 | 15-Jan-14 A | 24-Jan-14 A | |
| LL2-2011 | LL2 - F/R/P Pour #3 | 16 | 0 | 24-Jan-14 A | 18-Feb-14 A | |
| LL2-2019 | LL2 - F/R/P Pour #6 | 4 | 0 | 19-Feb-14 A | 17-Mar-14 A | |

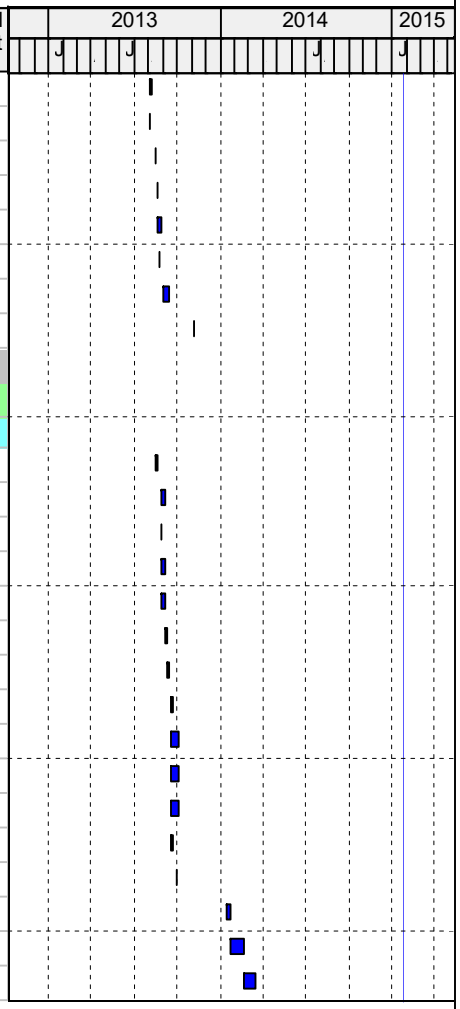



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2044 | LL2 - Set Generator | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |
| LL2-2004 | LL2 - Shore / Form Deck | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2035 | LL2 to LL1 - Shotcrete Walls | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2006 | LL2 - M & E Inserts | 4 | 0 | 14-Aug-13 A | 19-Aug-13 A | |
| LL2-2008 | LL2 - ReSteel / PT Cables | 6 | 0 | 14-Aug-13 A | 21-Aug-13 A | |
| LL2-2010 | LL2 - Install Embeds | 3 | 0 | 14-Aug-13 A | 16-Aug-13 A | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 0 | 27-Aug-13 A | 06-Sep-13 A | |
| LL2-2012 | LL2 - Place / Finish Deck | 3 | 0 | 29-Aug-13 A | 29-Aug-13 A | |
| LL2-2023 | LL2 - Waterproof Walls | 3 | 0 | 29-Aug-13 A | 03-Sep-13 A | |
| LL2-2014 | LL2 - Stress Tendons | 1 | 0 | 30-Aug-13 A | 30-Aug-13 A | |
| LL2-2016 | LL2 - Strip / ReShore | 3 | 0 | 03-Sep-13 A | 05-Sep-13 A | |
| LL2-8234 | LL2 - Place / Finish Deck | 3 | 0 | 12-Sep-13 A | 12-Sep-13 A | |
| LL2-2000 | LL2 - FRP Core Walls | 8 | 0 | 12-Sep-13 A | 23-Sep-13 A | |
| LL2-2018 | LL2 - Remove ReShores | 4 | 0 | 13-Nov-13 A | 18-Nov-13 A | |
| LL2-2013 | LL2 - F/R/P Pour #1 | 4 | 0 | 13-Jan-14 A | 16-Jan-14 A | |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| P5A-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2000 | LL1 - FRP Core Walls | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2004 | LL1 - Shore / Form Deck | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| P6-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P6-2004 | LL1 - Shore / Form Deck | 7 | 0 | 16-Sep-13 A | 24-Sep-13 A | |
| P5A-2006 | LL1 - MEP Rough In | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2008 | LL1 - ReSteel / PT Cables | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2012 | LL1 - Place / Finish Deck | 0 | 0 | 20-Sep-13 A | | |
| P5A-2020 | LL1 - Waterproof Walls | 3 | 0 | 20-Sep-13 A | 24-Sep-13 A | |

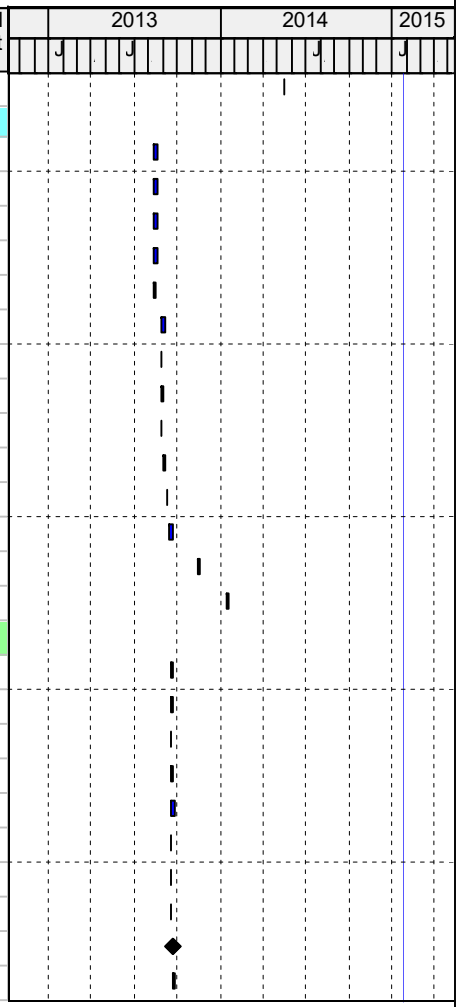


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P5A-2014 | LL1 - Stress Tendons | 1 | 0 | 23-Sep-13 A | 23-Sep-13 A | |
| P5A-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2006 | LL1 - MEP Rough In | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2008 | LL1 - ReSteel / PT Cables | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 24-Sep-13 A | 25-Sep-13 A | |
| P6-2020 | LL1 - Waterproof Walls | 4 | 0 | 24-Sep-13 A | 27-Sep-13 A | |
| P5A-2033 | LL1 - Resteel/Shotcrete Walls | 3 | 0 | 25-Sep-13 A | 27-Sep-13 A | |
| P5B-2002 | LL1 - FRP Columns Below | 5 | 0 | 26-Sep-13 A | 02-Oct-13 A | |
| P5B-2004 | LL1 - Shore / Form Deck | 7 | 0 | 26-Sep-13 A | 04-Oct-13 A | |
| P6-2012 | LL1 - Place / Finish Deck | 0 | 0 | 27-Sep-13 A | | |
| P6-2014 | LL1 - Stress Tendons | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2033 | LL1 - Resteel/Shotcrete Walls | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 01-Oct-13 A | 03-Oct-13 A | |
| P5B-2006 | LL1 - MEP Rough In | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2002 | FRP Columns Below | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2004 | Shore / Form Deck | 4 | 0 | 03-Oct-13 A | 08-Oct-13 A | |
| P5B-2008 | LL1 - ReSteel / PT Cables | 5 | 0 | 04-Oct-13 A | 10-Oct-13 A | |
| P5B-2010 | LL1 - Install Edgeform/Embeds | 4 | 0 | 04-Oct-13 A | 09-Oct-13 A | |
| P8-2002 | FRP Columns Below | 5 | 0 | 07-Oct-13 A | 11-Oct-13 A | |
| P8-2000 | Form/Resteel/Close Core Walls | 14 | 0 | 07-Oct-13 A | 24-Oct-13 A | |
| P8-2004 | Shore / Form Deck P8 | 8 | 0 | 07-Oct-13 A | 16-Oct-13 A | |
| P7-2002 | FRP Columns Below | 5 | 0 | 08-Oct-13 A | 14-Oct-13 A | |
| P7-2004 | Shore / Form Deck | 6 | 0 | 08-Oct-13 A | 15-Oct-13 A | |
| P10A--2006 | MEP Rough In | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2008 | ReSteel / PT Cables | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2010 | Install Edgeform/Embeds | 2 | 0 | 08-Oct-13 A | 09-Oct-13 A | |
| P5B-2012 | LL1 - Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |

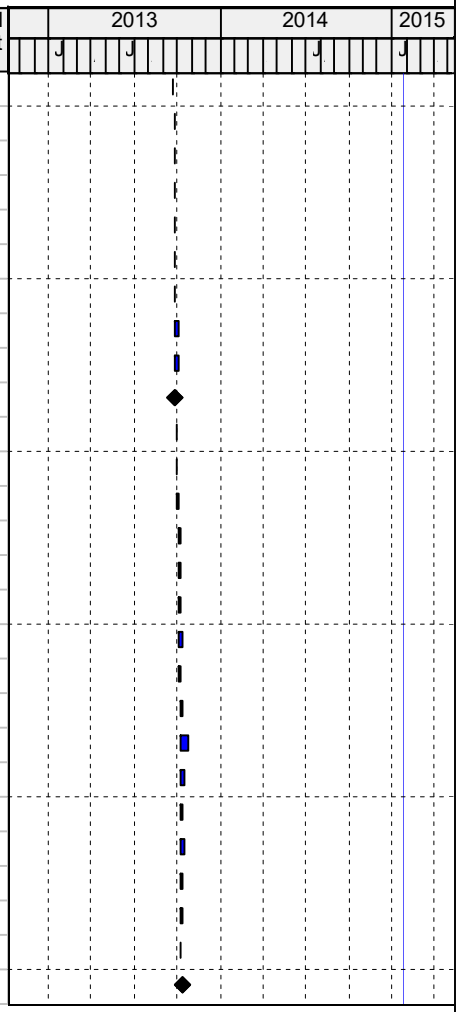



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P10A--2012 | Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P5B-2014 | LL1 - Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P7-2006 | MEP Rough In | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P7-2008 | ReSteel / PT Cables | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P10A--2014 | Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P8-2020 | Shore / Form Deck P9 | 6 | 0 | 14-Oct-13 A | 21-Oct-13 A | |
| P5B-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2010 | Install Edgeform/Embeds | 2 | 0 | 15-Oct-13 A | 16-Oct-13 A | |
| P8-2006 | MEP Rough In | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2008 | ReSteel / PT Cables | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2010 | Install Edgeform/Embeds | 4 | 0 | 15-Oct-13 A | 18-Oct-13 A | |
| P10A--2016 | Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2012 | Place / Finish Deck | 0 | 0 | 18-Oct-13 A | | |
| P7-2033 | Resteel/Shotcrete Walls | 3 | 0 | 18-Oct-13 A | 22-Oct-13 A | |
| P7-2014 | Stress Tendons | 1 | 0 | 21-Oct-13 A | 21-Oct-13 A | |
| P7-2016 | Strip / ReShore Deck | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2002 | FRP Columns Below | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P10B--2000 | FRP Shear Walls Below | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2004 | Shore / Form Deck | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P8-2012 | Place / Finish Deck P 8 & 9 and Core Walls | 0 | 0 | 25-Oct-13 A | | |
| P8-2014 | Stress Tendons | 1 | 0 | 28-Oct-13 A | 28-Oct-13 A | |
| P10B--2006 | MEP Rough In | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2008 | ReSteel / PT Cables | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2010 | Install Edgeform/Embeds | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P12--2002 | FRP Columns Below | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P12--2000 | Form/Resteel/Close Core Walls | 9 | 0 | 28-Oct-13 A | 07-Nov-13 A | |
| P12--2004 | Shore / Form Deck | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |

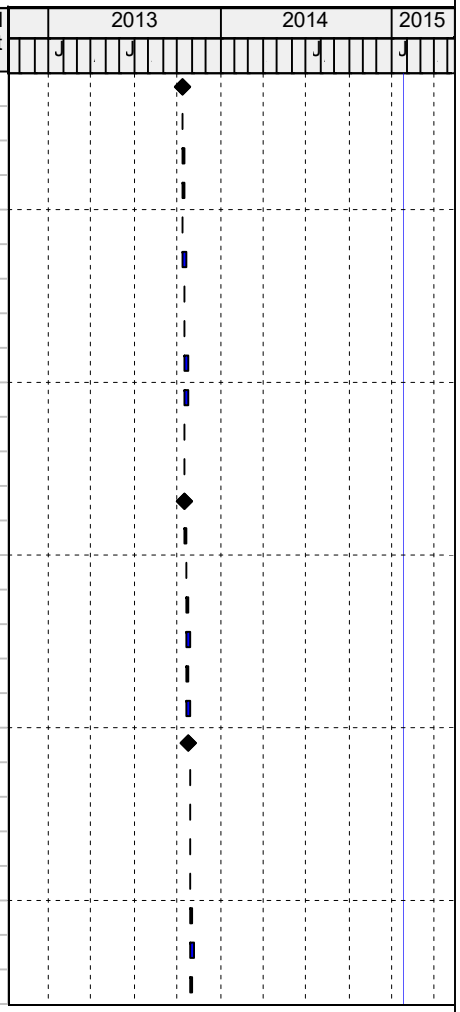



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P8-2016 | Strip / ReShore Deck | 3 | 0 | 29-Oct-13 A | 31-Oct-13 A | |
| P11–2002 | FRP Columns Below | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P11–2004 | Shore / Form Deck | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P10B–2012 | Place / Finish Deck | 0 | 0 | 31-Oct-13 A | | |
| P10B–2014 | Stress Tendons | 1 | 0 | 01-Nov-13 A | 01-Nov-13 A | |
| P12–2006 | MEP Rough In | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12–2008 | ReSteel / PT Cables | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12–2010 | Install Edgeform/Embeds | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P10B–2016 | Strip / ReShore Deck | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2006 | MEP Rough In | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2008 | ReSteel / PT Cables | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2010 | Install Edgeform/Embeds | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2012 | Place / Finish Deck | 0 | 0 | 07-Nov-13 A | | |
| P13–2002 | FRP Columns Below | 5 | 0 | 07-Nov-13 A | 14-Nov-13 A | |
| P13–2004 | Shore / Form Deck | 9 | 0 | 07-Nov-13 A | 28-Nov-13 A | |
| P11–2014 | Stress Tendons | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| P12–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 08-Nov-13 A | | |
| P11–2016 | Strip / ReShore Deck | 3 | 0 | 12-Nov-13 A | 14-Nov-13 A | |
| P12–2014 | Stress Tendons | 1 | 0 | 12-Nov-13 A | 12-Nov-13 A | |
| P14–2002 | FRP Columns Below | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P14–2000 | Form/Resteel/Close Core Walls | 8 | 0 | 19-Nov-13 A | 03-Dec-13 A | |
| P14–2004 | Shore / Form Deck | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P13A–2002 | FRP Columns Below | 5 | 0 | 21-Nov-13 A | 27-Nov-13 A | |
| P13A–2004 | Shore / Form Deck | 4 | 0 | 21-Nov-13 A | 26-Nov-13 A | |
| P13–2010 | Install Edgeform/Embeds | 5 | 0 | 22-Nov-13 A | 04-Dec-13 A | |
| P13–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2006 | MEP Rough In | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |

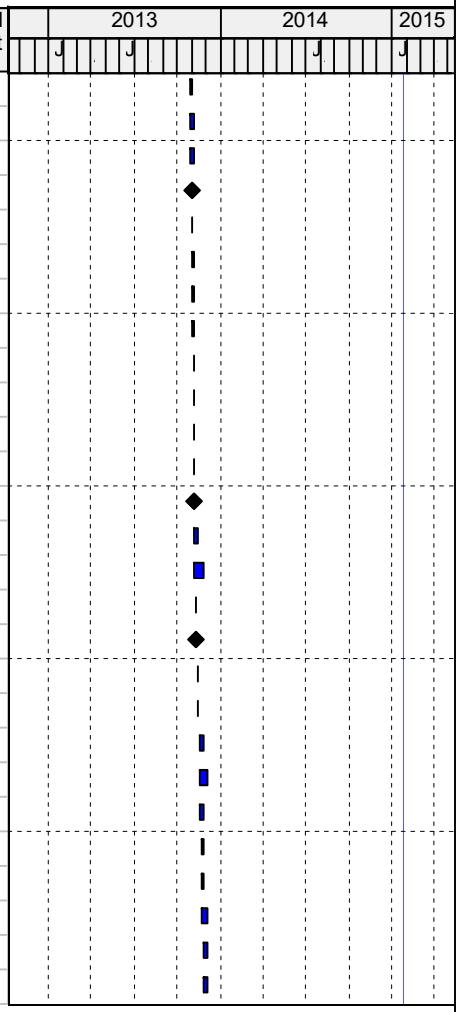



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P14–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2010 | Install Edgeform/Embeds | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P13–2006 | MEP Rough In | 5 | 0 | 26-Nov-13 A | 03-Dec-13 A | |
| P13A–2006 | MEP Rough In | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2008 | ReSteel / PT Cables | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2010 | Install Edgeform/Embeds | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13–2012 | Place / Finish Deck | 0 | 0 | 02-Dec-13 A | | |
| P13A–2012 | Place / Finish Deck | 0 | 0 | 03-Dec-13 A | | |
| P14–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 04-Dec-13 A | | |
| P13–2014 | Stress Tendons | 1 | 0 | 05-Dec-13 A | 05-Dec-13 A | |
| P15–2002 | FRP Columns Below | 3 | 0 | 05-Dec-13 A | 09-Dec-13 A | |
| P15–2000 | Jump/Resteel/Close Core | 9 | 0 | 05-Dec-13 A | 17-Dec-13 A | |
| P15–2004 | Shore / Form Deck | 5 | 0 | 05-Dec-13 A | 11-Dec-13 A | |
| P13–2016 | Strip / ReShore Deck | 3 | 0 | 06-Dec-13 A | 10-Dec-13 A | |
| P13A–2014 | Stress Tendons | 1 | 0 | 06-Dec-13 A | 06-Dec-13 A | |
| P14–2014 | Stress Tendons | 1 | 0 | 07-Dec-13 A | 07-Dec-13 A | |
| P15–2006 | MEP Rough In | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2008 | ReSteel / PT Cables | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2010 | Install Edgeform/Embeds | 3 | 0 | 11-Dec-13 A | 13-Dec-13 A | |
| P16-2002 | FRP Columns Below | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P16-2004 | Shore / Form Deck | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P15–2012 | Place / Finish Deck | 0 | 0 | 18-Dec-13 A | | |
| P15–2020 | Place Conc @ Core | 0 | 0 | 18-Dec-13 A | | |
| P16-2000 | Jump/Resteel/Close Core | 5 | 0 | 18-Dec-13 A | 24-Dec-13 A | |
| P16-2006 | MEP Rough In | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2008 | ReSteel / PT Cables | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2010 | Install Edgeform/Embeds | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |

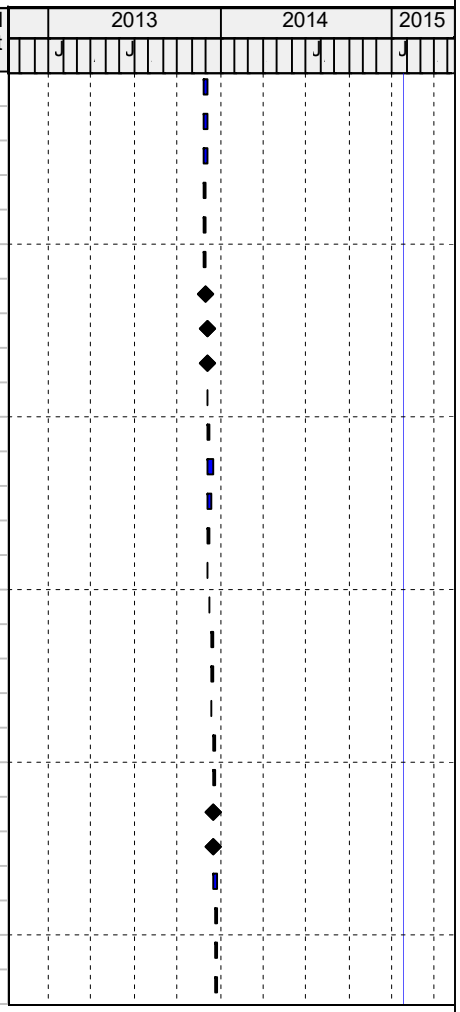



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P15–2014 | Stress Tendons | 1 | 0 | 21-Dec-13 A | 21-Dec-13 A | |
| P8-2018 | Remove Reshores | 2 | 0 | 23-Dec-13 A | 24-Dec-13 A | |
| P10A–2018 | Remove Reshores | 2 | 0 | 26-Dec-13 A | 27-Dec-13 A | |
| P16-2012 | Place / Finish Deck | 0 | 0 | 26-Dec-13 A | | |
| P16-2020 | Place Conc @ Core | 0 | 0 | 26-Dec-13 A | | |
| P17-2002 | FRP Columns Below | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P17-2000 | Jump/Resteel/Close Core | 7 | 0 | 27-Dec-13 A | 07-Jan-14 A | |
| P17-2004 | Shore / Form Deck | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P10B–2018 | Remove Reshores | 2 | 0 | 30-Dec-13 A | 31-Dec-13 A | |
| P16-2014 | Stress Tendons | 1 | 0 | 31-Dec-13 A | 31-Dec-13 A | |
| P5A-2018 | LL1 - Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P11–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P12–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P17-2006 | MEP Rough In | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2008 | ReSteel / PT Cables | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2010 | Install Edgeform/Embeds | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P6-2018 | LL1 - Remove Reshores | 2 | 0 | 06-Jan-14 A | 07-Jan-14 A | |
| P5B-2018 | LL1 - Remove Reshores | 2 | 0 | 08-Jan-14 A | 09-Jan-14 A | |
| P17-2012 | Place / Finish Deck | 0 | 0 | 08-Jan-14 A | | |
| P17-2020 | Place Conc @ Core | 0 | 0 | 08-Jan-14 A | | |
| P18-2002 | FRP Columns Below | 5 | 0 | 09-Jan-14 A | 15-Jan-14 A | |
| P18-2000 | Jump/Resteel/Close Core | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P18-2004 | Shore / Form Deck | 3 | 0 | 09-Jan-14 A | 13-Jan-14 A | |
| LL2-2022R | MEP Rough In | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P7-2018 | Remove Reshores | 2 | 0 | 10-Jan-14 A | 13-Jan-14 A | |
| P17-2014 | Stress Tendons | 1 | 0 | 11-Jan-14 A | 11-Jan-14 A | |
| P13–2018 | Remove Reshores | 2 | 0 | 13-Jan-14 A | 14-Jan-14 A | |

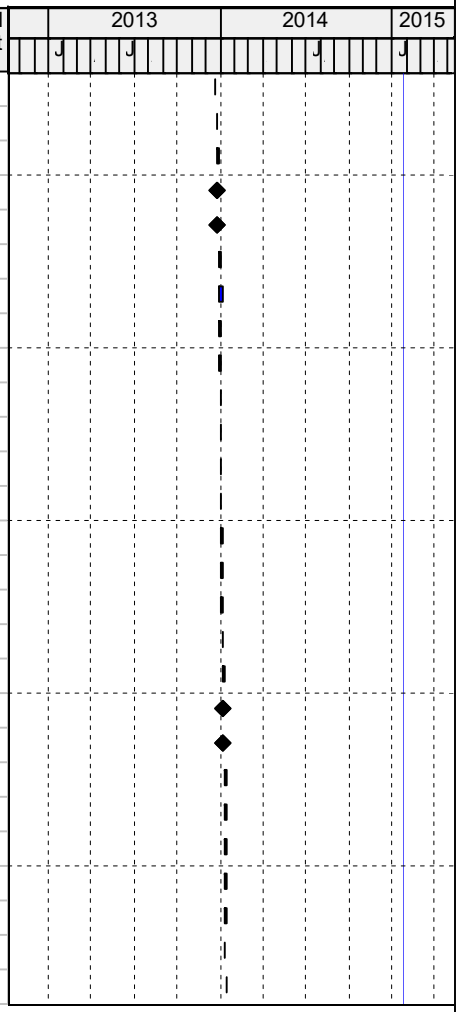



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P13A--2018 | Remove Reshores | 2 | 0 | 15-Jan-14 A | 16-Jan-14 A | |
| WEA-2012 | WIND IMPACT | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| P18-2006 | MEP Rough In | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2008 | ReSteel / PT Cables | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2010 | Install Edgeform/Embeds | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2012 | Place / Finish Deck | 0 | 0 | 22-Jan-14 A | | |
| P18-2020 | Place Conc @ Core | 0 | 0 | 22-Jan-14 A | | |
| P19-2002 | FRP Columns Below | 5 | 0 | 23-Jan-14 A | 29-Jan-14 A | |
| P19-2000 | Jump/Resteel/Close Core | 4 | 0 | 23-Jan-14 A | 28-Jan-14 A | |
| P19-2004 | Shore / Form Deck | 3 | 0 | 23-Jan-14 A | 27-Jan-14 A | |
| P18-2014 | Stress Tendons | 1 | 0 | 25-Jan-14 A | 25-Jan-14 A | |
| P14--2018 | Remove Reshores | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2006 | MEP Rough In | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2008 | ReSteel / PT Cables | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2010 | Install Edgeform/Embeds | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2012 | Place / Finish Deck | 0 | 0 | 29-Jan-14 A | | |
| P19-2020 | Place Conc @ Core | 0 | 0 | 29-Jan-14 A | | |
| P20-2002 | FRP Columns Below | 5 | 0 | 30-Jan-14 A | 05-Feb-14 A | |
| P20-2000 | Jump/Resteel/Close Core | 9 | 0 | 30-Jan-14 A | 11-Feb-14 A | |
| P20-2004 | Shore / Form Deck | 6 | 0 | 30-Jan-14 A | 10-Feb-14 A | |
| P19-2014 | Stress Tendons | 1 | 0 | 01-Feb-14 A | 01-Feb-14 A | |
| P13A--2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P14--2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P15--2016 | Strip / ReShore Deck | 3 | 0 | 06-Feb-14 A | 10-Feb-14 A | |
| P20-2006 | MEP Rough In | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2008 | ReSteel / PT Cables | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2010 | Install Edgeform/Embeds | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |

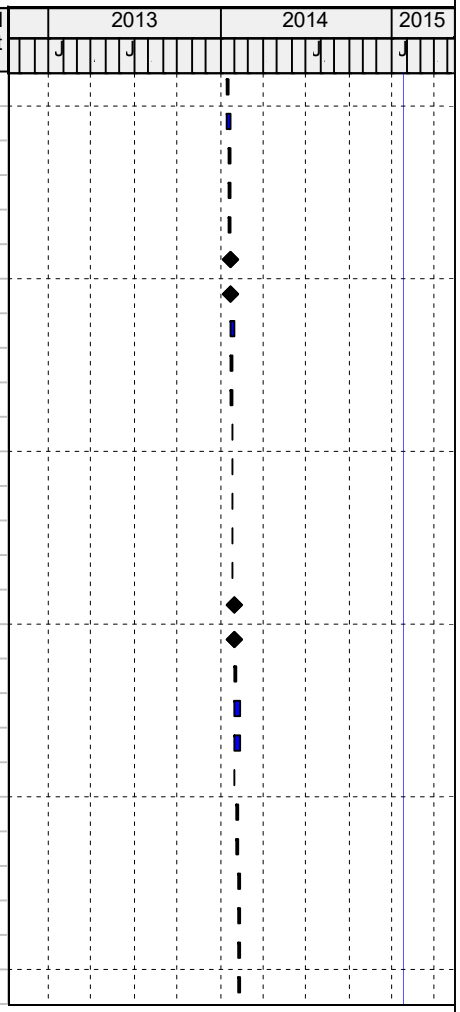



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 06-Feb-14 A | 12-Feb-14 A | |
| P16-2016 | Strip / ReShore Deck | 3 | 0 | 10-Feb-14 A | 12-Feb-14 A | |
| L04-2018 | Remove Reshores | 2 | 0 | 10-Feb-14 A | 11-Feb-14 A | |
| L03-2018 | Remove Reshores | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| P17-2016 | Strip / ReShore Deck | 3 | 0 | 12-Feb-14 A | 14-Feb-14 A | |
| P20-2012 | Place / Finish Deck | 0 | 0 | 12-Feb-14 A | | |
| P20-2020 | Place Conc @ Core | 0 | 0 | 12-Feb-14 A | | |
| L04-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-Feb-14 A | 18-Feb-14 A | |
| P12–2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P18-2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P21-2002 | FRP Columns Below | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| P21-2000 | Jump/Resteel/Close Core | 4 | 0 | 13-Feb-14 A | 18-Feb-14 A | |
| P21-2004 | Shore / Form Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P19-2016 | Strip / ReShore Deck | 3 | 0 | 14-Feb-14 A | 18-Feb-14 A | |
| P20-2014 | Stress Tendons | 1 | 0 | 15-Feb-14 A | 15-Feb-14 A | |
| P21-2006 | MEP Rough In | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2008 | ReSteel / PT Cables | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P20-2016 | Strip / ReShore Deck | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| L05-2018 | Remove Reshores | 2 | 0 | 18-Feb-14 A | 19-Feb-14 A | |
| P21-2012 | Place / Finish Deck | 0 | 0 | 19-Feb-14 A | | |
| P21-2020 | Place Conc @ Core | 0 | 0 | 19-Feb-14 A | | |
| P22-2002 | FRP Columns Below | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P22-2000 | Jump/Resteel/Close Core | 4 | 0 | 20-Feb-14 A | 25-Feb-14 A | |
| P22-2004 | Shore / Form Deck | 3 | 0 | 20-Feb-14 A | 24-Feb-14 A | |
| L05-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P21-2014 | Stress Tendons | 1 | 0 | 22-Feb-14 A | 22-Feb-14 A | |

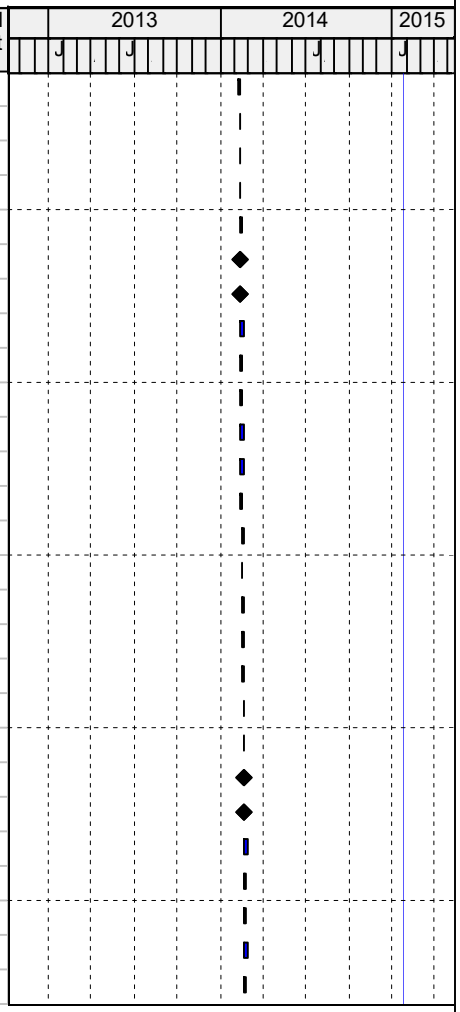



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P21-2016 | Strip / ReShore Deck | 3 | 0 | 24-Feb-14 A | 26-Feb-14 A | |
| P22-2006 | MEP Rough In | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2008 | ReSteel / PT Cables | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| L06-2018 | Remove Reshores | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| P22-2012 | Place / Finish Deck | 0 | 0 | 26-Feb-14 A | | |
| P22-2020 | Place Conc @ Core | 0 | 0 | 26-Feb-14 A | | |
| P23-2002 | FRP Columns Below | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2000 | Jump/Resteel/Close Core | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2004 | Shore / Form Deck | 3 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2006 | MEP Rough In | 2 | 0 | 01-Mar-14 A | 03-Mar-14 A | |
| P22-2014 | Stress Tendons | 1 | 0 | 01-Mar-14 A | 01-Mar-14 A | |
| P23-2008 | ReSteel / PT Cables | 2 | 0 | 03-Mar-14 A | 04-Mar-14 A | |
| P22-2016 | Strip / ReShore Deck | 3 | 0 | 04-Mar-14 A | 10-Mar-14 A | |
| P23-2010 | Install Edgeform/Embeds | 2 | 0 | 04-Mar-14 A | 04-Mar-14 A | |
| L07-2018 | Remove Reshores | 2 | 0 | 04-Mar-14 A | 05-Mar-14 A | |
| P23-2012 | Place / Finish Deck | 0 | 0 | 05-Mar-14 A | | |
| P23-2020 | Place Conc @ Core | 0 | 0 | 05-Mar-14 A | | |
| P24-2002 | FRP Columns Below | 5 | 0 | 05-Mar-14 A | 07-Mar-14 A | |
| P24-2004 | Shore / Form Deck | 3 | 0 | 06-Mar-14 A | 10-Mar-14 A | |
| P24-2000 | Jump/Resteel/Close Core | 4 | 0 | 08-Mar-14 A | 10-Mar-14 A | |
| P23-2014 | Stress Tendons | 1 | 0 | 10-Mar-14 A | 10-Mar-14 A | |
| P24-2008 | ReSteel / PT Cables | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P24-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P23-2016 | Strip / ReShore Deck | 3 | 0 | 11-Mar-14 A | 17-Mar-14 A | |
| P24-2006 | MEP Rough In | 2 | 0 | 11-Mar-14 A | 11-Mar-14 A | |
| P25-2002 | FRP Columns Below | 5 | 0 | 11-Mar-14 A | 13-Mar-14 A | |

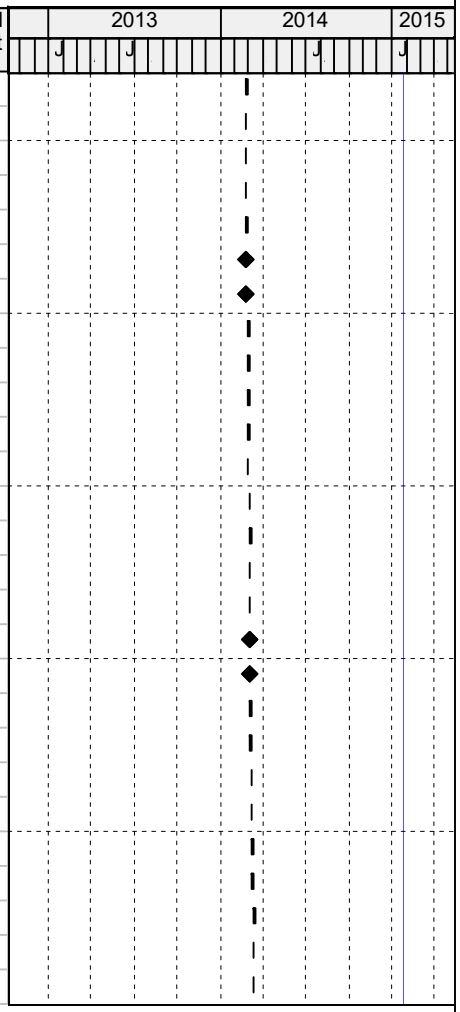


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-2018 | Remove Reshores | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| P24-2012 | Place / Finish Deck | 0 | 0 | 12-Mar-14 A | | |
| P24-2020 | Place Conc @ Core | 0 | 0 | 12-Mar-14 A | | |
| P25-2004 | Shore / Form Deck | 3 | 0 | 13-Mar-14 A | 17-Mar-14 A | |
| P25-2000 | Jump/Resteel/Close Core | 4 | 0 | 15-Mar-14 A | 17-Mar-14 A | |
| P24-2014 | Stress Tendons | 1 | 0 | 17-Mar-14 A | 17-Mar-14 A | |
| P25-2006 | MEP Rough In | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2008 | ReSteel / PT Cables | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| L06-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 18-Mar-14 A | 20-Mar-14 A | |
| L09-2018 | Remove Reshores | 2 | 0 | 18-Mar-14 A | 19-Mar-14 A | |
| P26-2002 | FRP Columns Below | 5 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| P25-2012 | Place / Finish Deck | 0 | 0 | 19-Mar-14 A | | |
| P25-2020 | Place Conc @ Core | 0 | 0 | 19-Mar-14 A | | |
| P26-2004 | Shore / Form Deck | 3 | 0 | 20-Mar-14 A | 24-Mar-14 A | |
| L07-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 21-Mar-14 A | 25-Mar-14 A | |
| P26-2000 | Jump/Resteel/Close Core | 4 | 0 | 22-Mar-14 A | 24-Mar-14 A | |
| P26-2006 | MEP Rough In | 2 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P26-2008 | ReSteel / PT Cables | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P26-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P25-2014 | Stress Tendons | 1 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P27-2002 | FRP Columns Below | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| P26-2012 | Place / Finish Deck | 0 | 0 | 26-Mar-14 A | | |
| P26-2020 | Place Conc @ Core | 0 | 0 | 26-Mar-14 A | | |
| L08-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 26-Mar-14 A | 28-Mar-14 A | |
| L10-2018 | Remove Reshores | 2 | 0 | 26-Mar-14 A | 27-Mar-14 A | |
| P27-2004 | Shore / Form Deck | 3 | 0 | 27-Mar-14 A | 31-Mar-14 A | |

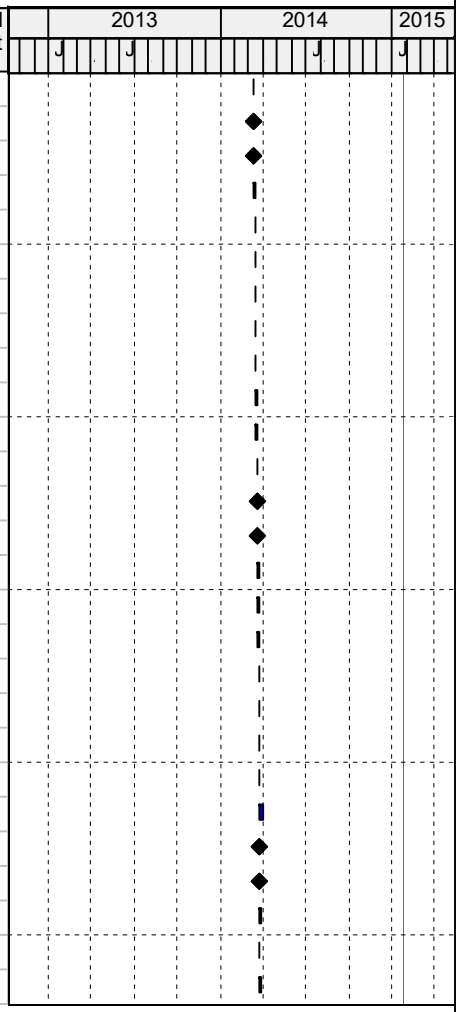



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P27-2000 | Jump/Resteel/Close Core | 4 | 0 | 29-Mar-14 A | 31-Mar-14 A | |
| P27-2006 | MEP Rough In | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2008 | ReSteel / PT Cables | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2010 | Install Edgeform/Embeds | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P26-2014 | Stress Tendons | 1 | 0 | 31-Mar-14 A | 31-Mar-14 A | |
| L09-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 31-Mar-14 A | 02-Apr-14 A | |
| P24-2016 | Strip / ReShore Deck | 3 | 0 | 01-Apr-14 A | 07-Apr-14 A | |
| L11-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 02-Apr-14 A | |
| L12-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 03-Apr-14 A | |
| P27-2012 | Place / Finish Deck | 0 | 0 | 02-Apr-14 A | | |
| P27-2020 | Place Conc @ Core | 0 | 0 | 02-Apr-14 A | | |
| P28-2002 | FRP Columns Below | 5 | 0 | 02-Apr-14 A | 04-Apr-14 A | |
| P28-2004 | Shore / Form Deck | 4 | 0 | 03-Apr-14 A | 08-Apr-14 A | |
| L10-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| P27-2014 | Stress Tendons | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| P25-2016 | Strip / ReShore Deck | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L14-2018 | Remove Reshores | 2 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| P28-2000 | Jump/Resteel/Close Core | 7 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| P28-2006 | MEP Rough In | 4 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2008 | ReSteel / PT Cables | 4 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Apr-14 A | 11-Apr-14 A | |
| L12-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| P28-2012 | Place / Finish Deck | 0 | 0 | 14-Apr-14 A | | |
| P28-2020 | Place Conc @ Core | 0 | 0 | 14-Apr-14 A | | |
| P29-2002 | FRP Columns Above Roof Deck | 3 | 0 | 14-Apr-14 A | 18-Apr-14 A | |
| P26-2016 | Strip / ReShore Deck | 3 | 0 | 14-Apr-14 A | 17-Apr-14 A | |

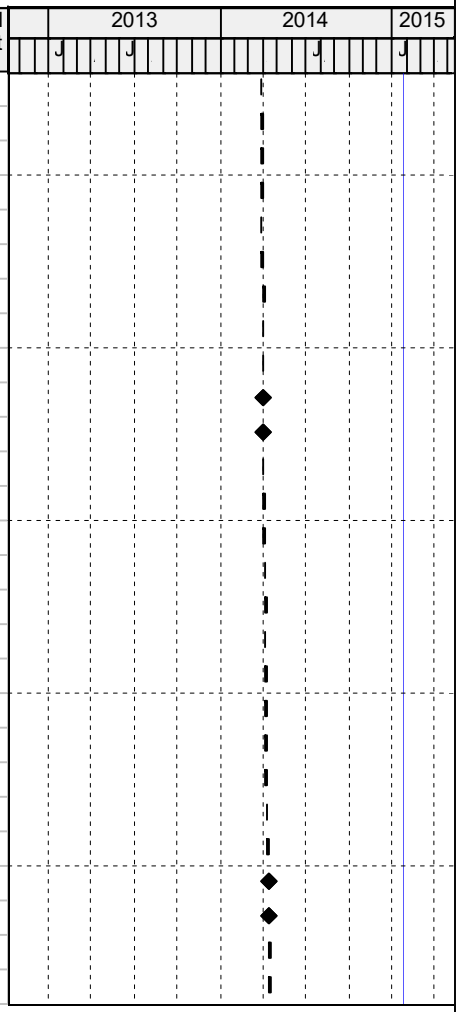



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-Apr-14 A | 18-Apr-14 A | |
| P28-2014 | Stress Tendons | 1 | 0 | 17-Apr-14 A | 17-Apr-14 A | |
| P29-2000 | Strip Core | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| P27-2016 | Strip / ReShore Deck | 3 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L15-2018 | Remove Reshores | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| P28-2016 | Strip / ReShore Deck | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L15-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L16-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-May-14 A | 19-May-14 A | |
| L16-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2019 | Grind Ceiling for Skim Coat | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| **Ballroom Catwalk & Roof** | | | | | | |
| PC-2100 | Erect Structural Steel @ Porte Cochere | 3 | 0 | 30-Jan-14 A | 03-Feb-14 A | |
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 7 | 0 | 07-Feb-14 A | 17-Feb-14 A | |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| PC-2102 | Metal Decking @ Porte Cochere/ Roof | 2 | 0 | 17-Apr-14 A | 18-Apr-14 A | |
| BR-2112 | BR - Fireproofing @ Structural Steel | 2 | 0 | 27-May-14 A | 30-May-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Mech Penthouse** | | | | | | |
| PH-8706 | Set Mech Equipment @ Tower Roof | 3 | 0 | 22-May-14 A | 28-May-14 A | |
| PH-8708 | Set Equipment @ Penthouse | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| PH-8700 | PH - Structural Steel and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| **Vertical Circulation** | | | | | | |
| **Stairs** | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 25-Nov-13 A | 26-Nov-13 A | |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 27-Nov-13 A | 03-Dec-13 A | |

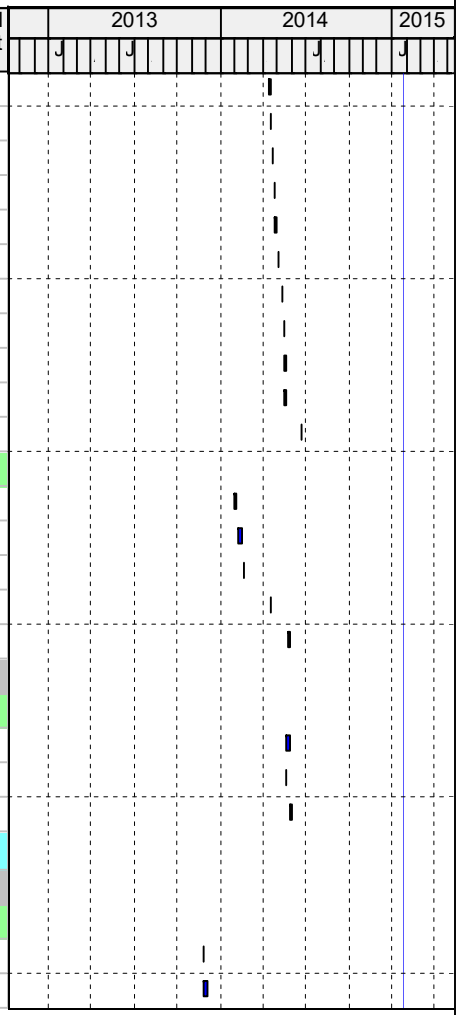



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 04-Dec-13 A | 05-Dec-13 A | |
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 06-Dec-13 A | 09-Dec-13 A | |
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 2 | 0 | 03-Feb-14 A | 04-Feb-14 A | |
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 2 | 0 | 06-Feb-14 A | 07-Feb-14 A | |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 2 | 0 | 07-Feb-14 A | 07-Feb-14 A | |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 2 | 0 | 07-Feb-14 A | 10-Feb-14 A | |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 2 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 2 | 0 | 06-Mar-14 A | 07-Mar-14 A | |
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 2 | 0 | 07-Mar-14 A | 10-Mar-14 A | |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 2 | 0 | 13-Mar-14 A | 14-Mar-14 A | |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 2 | 0 | 08-Apr-14 A | 21-Apr-14 A | |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| S1-4040 | Stair 1 - Set Mtl Stairs / Railings L18 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 10-Dec-13 A | 11-Dec-13 A | |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 12-Dec-13 A | 13-Dec-13 A | |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 16-Dec-13 A | 17-Dec-13 A | |
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 18-Dec-13 A | 19-Dec-13 A | |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 2 | 0 | 12-Feb-14 A | 13-Feb-14 A | |
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 2 | 0 | 13-Feb-14 A | 13-Feb-14 A | |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 2 | 0 | 13-Feb-14 A | 14-Feb-14 A | |

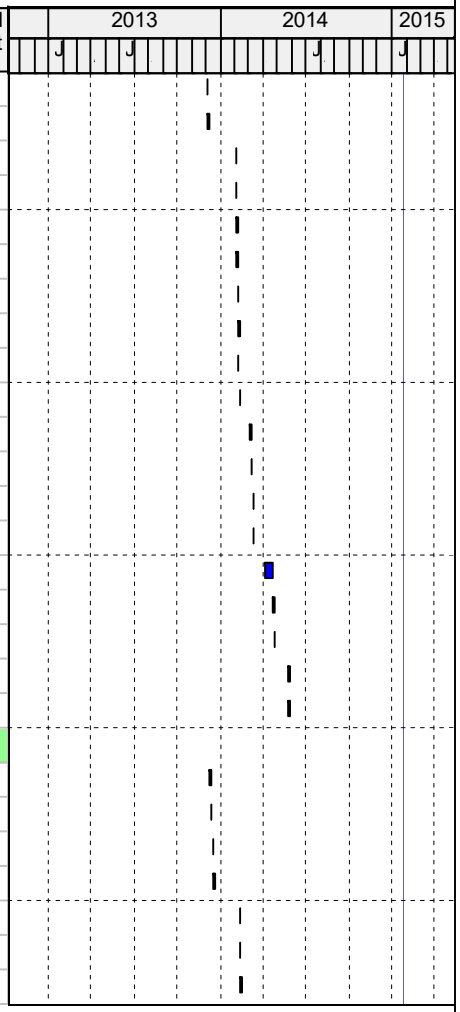



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 2 | 0 | 19-Feb-14 A | 20-Feb-14 A | |
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 2 | 0 | 21-Feb-14 A | 24-Feb-14 A | |
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 2 | 0 | 19-Mar-14 A | 20-Mar-14 A | |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 2 | 0 | 21-Mar-14 A | 22-Mar-14 A | |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 2 | 0 | 14-May-14 A | 15-May-14 A | |
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 2 | 0 | 16-May-14 A | 19-May-14 A | |
| S2-4038 | Stair 2 - Set Mtl Stairs / Railings L17 | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - Set Metal Stairs / Railings LL2 | 6 | 0 | 05-Mar-14 A | 20-Mar-14 A | |
| S3-4002 | Stair 3 - Set Metal Stairs / Railings LL1 | 6 | 0 | 17-Mar-14 A | 21-Mar-14 A | |
| S3-4004 | Stair 3 - Permanent Railings / Final Finishes | 4 | 4 | 11-Mar-15 | 16-Mar-15 | 27 |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |
| S4-4000 | Stair 4 - Set Metal Stairs / Railings LL2 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4002 | Stair 4 - Set Metal Stairs / Railings LL1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4004 | Stair 4 -Set Metal Stairs / Railings L1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4006 | Stair 4 - Permanent Railings / Final Finishes | 4 | 4 | 09-Mar-15 | 12-Mar-15 | 27 |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |
| S6-4000 | Stair 6 - Set Metal Stairs / Railings | 5 | 0 | 25-Jun-14 A | 01-Jul-14 A | |
| S6-4002 | Stair 6 - Permanent Railings / Final Finishes | 2 | 2 | 06-Feb-15 | 09-Feb-15 | 52 |
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |

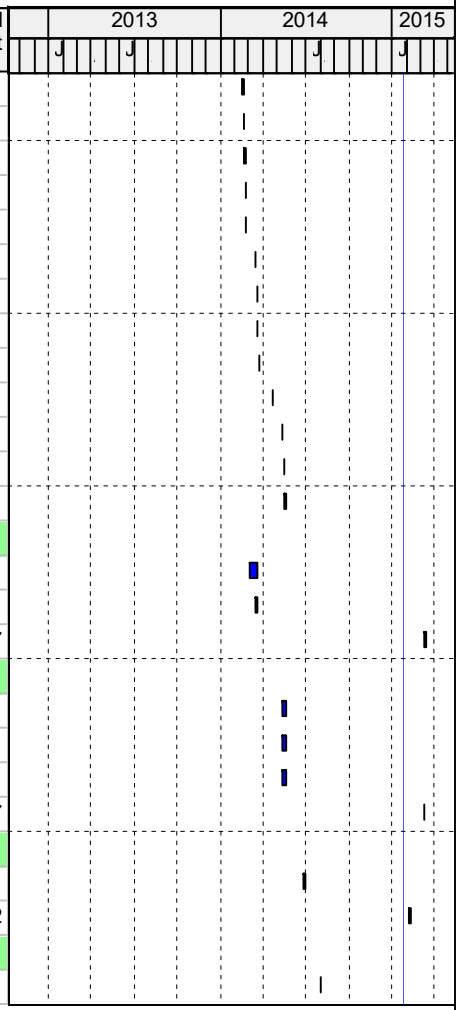



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes | 5 | 5 | 07-Apr-15 | 13-Apr-15 | 7 |
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a -Set Metal Stairs / Railings L1 | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| S4a-4002 | Stair 4a - Permanent Railings / Final Finishes | 2 | 2 | 13-Mar-15 | 16-Mar-15 | 27 |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 07-Jun-13 A | | |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 0 | 17-Jun-13 A | 21-Jun-13 A | |
| EL-1004 | Elev - Submittal Approval | 21 | 0 | 21-Jun-13 A | 01-Jan-14 A | |
| EL-1006 | Elev - Release to Manufacturing | 14 | 0 | 02-Jan-14 A | 15-Jan-14 A | |
| EL-1008 | Elev - Fabrication (Engineered Geared) | 95 | 0 | 16-Jan-14 A | 14-Jun-14 A | |
| EL-1010 | Elev - Machines delivered | 1 | 0 | 12-May-14 A | 12-May-14 A | |
| EL-1011 | Elev - Elevator Machines Flown & Set At Top Of Hoist | 5 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5016 | Elev 5 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-1216 | Elev 1&2 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-3416 | Elev 3&4 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-1202 | Elev 1&2 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-3402 | Elev 3&4 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-5018 | Elev 5 - Set Hoistway Machines | 3 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| EL-1218 | Elev 1&2 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-3418 | Elev 3&4 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-1200 | Elev 1&2 - Hoistway Clear & Ready (GC) | 0 | 0 | 20-Jun-14 A | | |
| EL-1204 | Elev 1&2 - Install Rails & Brackets | 17 | 0 | 23-Jun-14 A | 15-Jul-14 A | |
| EL-3400 | Elev 3&4 - Hoistway Clear & Ready (GC) | 0 | 0 | 23-Jun-14 A | | |

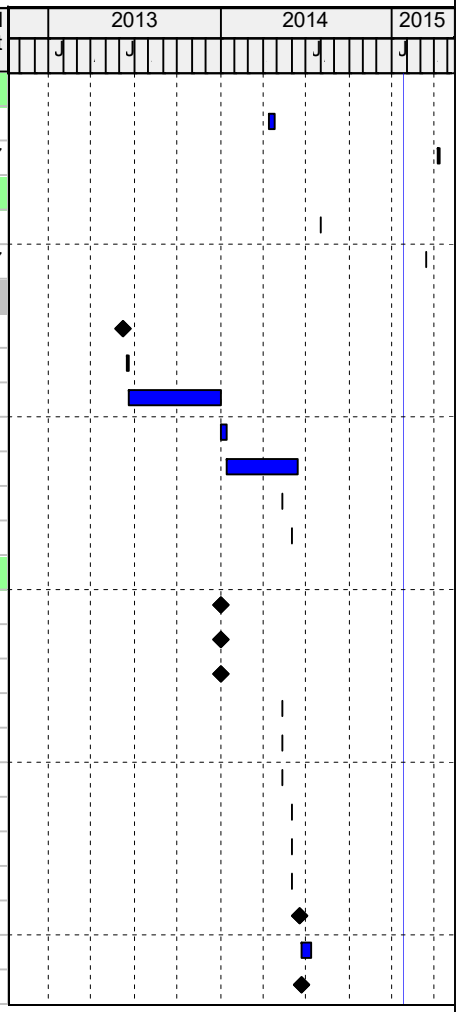


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 24-Jun-14 A | | |
| EL-1206 | Elev 1&2 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Jul-14 A | |
| EL-1207 | Elev 1&2 - Install Pit Equipment/Car Sling/CWT Fram | 3 | 0 | 15-Jul-14 A | 01-Aug-14 A | |
| EL-1208 | Elev 1&2 - Install MHoist & Cable | 5 | 0 | 16-Jul-14 A | 24-Jul-14 A | |
| EL-3407 | Elev 3&4 - Install Pit Equipment/Car Sling/CWT Fram | 5 | 0 | 16-Jul-14 A | 06-Aug-14 A | |
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 21-Jul-14 A | | |
| EL-5004 | Elev 5 - Install Rails & Brackets | 13 | 0 | 21-Jul-14 A | 11-Aug-14 A | |
| EL-3404 | Elev 3&4 - Install Rails & Brackets | 18 | 0 | 23-Jul-14 A | 04-Aug-14 A | |
| EL-3406 | Elev 3&4 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 28-Jul-14 A | |
| EL-3408 | Elev 3&4 - Install Hoist & Cable | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| EL-5007 | Elev 5 - Install Pit Equipment/Car Sling/CWT Frame/V | 5 | 0 | 12-Aug-14 A | 15-Aug-14 A | |
| EL-1210 | Elev 1&2 - Install Entrances/Doors/Fixtures/Fascia | 19 | 0 | 14-Aug-14 A | 22-Sep-14 A | |
| EL-3410 | Elev 3&4 - Install Entrances/Doors/Fixtures/Fascia | 30 | 0 | 14-Aug-14 A | 02-Oct-14 A | |
| EL-5006 | Elev 5 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Aug-14 A | |
| EL-5008 | Elev 5 - Install MHoist & Cable | 4 | 0 | 18-Aug-14 A | 20-Aug-14 A | |
| EL-5010 | Elev 5 - Install Entrances/Doors/Fixtures/Fascia | 21 | 0 | 21-Aug-14 A | 26-Sep-14 A | |
| EL-1212 | Elev 1&2 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 22-Sep-14 A | 13-Oct-14 A | |
| EL-5012 | Elev 5 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 26-Sep-14 A | 16-Oct-14 A | |
| EL-3412 | Elev 3&4 - Install Hoistway Equipment/Pipe & Wire | 23 | 0 | 03-Oct-14 A | 03-Nov-14 A | |
| EL-1214 | Elev 1&2 - Install Cab/Wiring/Door Operator(s) | 11 | 0 | 14-Oct-14 A | 28-Oct-14 A | |
| EL-5014 | Elev 5 - Install Cab/Wiring/Door Operator(s) | 7 | 0 | 17-Oct-14 A | 27-Oct-14 A | |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 1 | 0 | 24-Oct-14 A | 24-Oct-14 A | |
| EL-6016 | Elev 6 - Hoistway Walls Complete (GC) | 0 | 0 | | 24-Oct-14 A | |
| EL-6004 | Elev 6 - Install Cylinders/Rails & Brackets | 4 | 0 | 27-Oct-14 A | 30-Oct-14 A | |
| EL-5022 | Elev 5 - Adjust | 5 | 0 | 28-Oct-14 A | 03-Nov-14 A | |
| EL-1222 | Elev 1&2 - Adjust | 5 | 0 | 29-Oct-14 A | 04-Nov-14 A | |
| EL-6006 | Elev 6 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 30-Oct-14 A | |

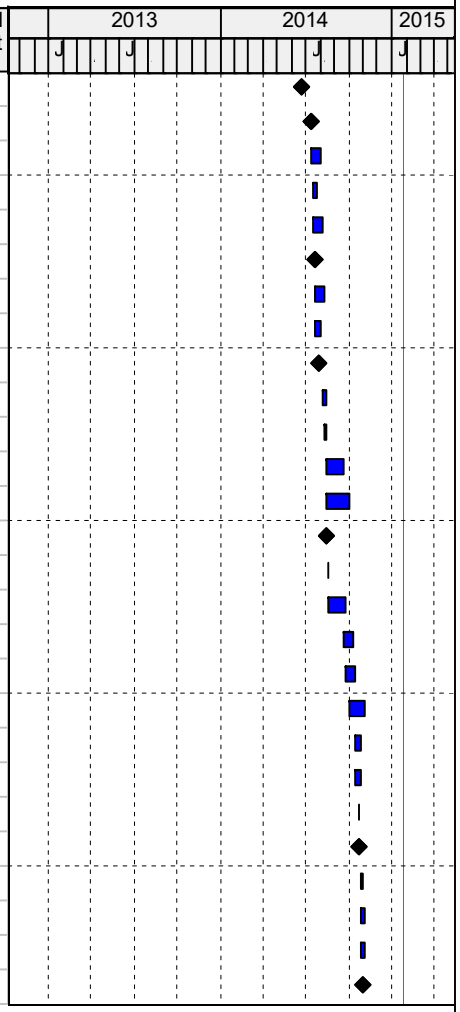



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6007 | Elev 6 - Install Pit Equipment/Car Sling | 2 | 0 | 31-Oct-14 A | 03-Nov-14 A | |
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| EL-3414 | Elev 3&4 - Install Cab/Wiring/Door Operator(s) | 10 | 0 | 04-Nov-14 A | 17-Nov-14 A | |
| EL-6018 | Elev 6 - Install Machine Room Equipment | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| EL-1224 | Elev 1&2 - Clean / Paint / Punchlist | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| EL-5026 | Elev 5 - Inspections | 7 | 0 | 13-Nov-14 A | 14-Nov-14 A | |
| EL-3422 | Elev 3&4 - Adjust | 8 | 0 | 18-Nov-14 A | 20-Nov-14 A | |
| EL-6012 | Elev 6 - Install hoistway rails & divider beams | 2 | 0 | 20-Nov-14 A | 21-Nov-14 A | |
| EL-6010 | Elev 6 - Install elevator fronts/rears | 9 | 0 | 09-Dec-14 A | 24-Dec-14 A | |
| EL-6014 | Elev 6 - Cab build-out | 5 | 1 | 15-Dec-14 A | 30-Jan-15 | 37 |
| EL-3424 | Elev 3&4 - Walsh/TKE pre-inspection | 6 | 6 | 26-Jan-15 | 02-Feb-15 | 27 |
| EL-6022 | Elev 6 - Final cleaning at EMR | 4 | 4 | 06-Feb-15 | 11-Feb-15 | 37 |
| EL-1226 | Elev 1&2 - CoB/L&I Inspections | 5 | 5 | 09-Feb-15* | 13-Feb-15 | 23 |
| EL-3426 | Elev 3&4 - CoB/L&I Inspections | 5 | 5 | 09-Feb-15 | 13-Feb-15 | 23 |
| EL-6024 | Elev 6 - Walsh/TKE pre-inspection | 2 | 2 | 12-Feb-15 | 13-Feb-15 | 37 |
| EL-6026 | Elev 6 - CoB/L&I Inspections | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 37 |
| **Exterior Shell** | | | | | | |
| **Elevations** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2** | | | | | | |
| L3D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Feb-14 A | 12-Feb-14 A | |
| L3-5308 | L3- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 17-Feb-14 A | 21-Feb-14 A | |
| L4D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Feb-14 A | 19-Feb-14 A | |
| L4-5308 | L4- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Feb-14 A | 28-Feb-14 A | |
| L5D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Feb-14 A | 26-Feb-14 A | |
| L5-5308 | L5- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 03-Mar-14 A | 07-Mar-14 A | |
| L6D5308 | Deliver/Stock Wall Panels | 1 | 0 | 05-Mar-14 A | 05-Mar-14 A | |

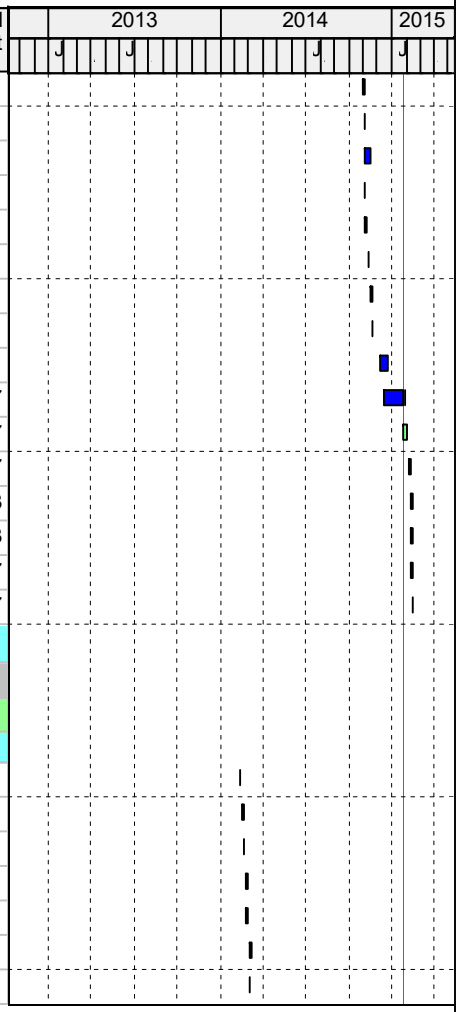


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L6-5308 | L6- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L7-5308 | L7- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L7D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Mar-14 A | 12-Mar-14 A | |
| L8D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Mar-14 A | 19-Mar-14 A | |
| L8-5308 | L8- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Mar-14 A | 28-Mar-14 A | |
| L9D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L9-5308 | L9- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 31-Mar-14 A | 07-Apr-14 A | |
| 10D5308 | Deliver/Stock Wall Panels | 1 | 0 | 02-Apr-14 A | 02-Apr-14 A | |
| L10-5308 | L10- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 07-Apr-14 A | 11-Apr-14 A | |
| 11D5308 | Deliver/Stock Wall Panels | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L11-5308 | L11- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 11-Apr-14 A | 18-Apr-14 A | |
| 12D5308 | Deliver/Stock Wall Panels | 1 | 0 | 16-Apr-14 A | 16-Apr-14 A | |
| L12-5308 | L12- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Apr-14 A | 25-Apr-14 A | |
| 14D5308 | Deliver/Stock Wall Panels | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L14-5308 | L14 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Apr-14 A | 01-May-14 A | |
| 15D5308 | Deliver/Stock Wall Panels | 1 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L15-5308 | L15 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| 16D5308 | Deliver/Stock Wall Panels | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L16-5308 | L16- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| 17D5308 | Deliver/Stock Wall Panels | 1 | 0 | 14-May-14 A | 14-May-14 A | |
| L17-5308 | L17 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 20-May-14 A | 11-Jun-14 A | |
| LL2-5308 | LL2 Thru L4 - Support Frame/Sheathing for Metal Wa | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL1-5308 | LL1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| L1-5308 | L1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| **Level 1** | | | | | | |
| L3-5102 | L3- Storefront Frames | 7 | 0 | 18-Aug-14 A | 29-Sep-14 A | |
| L1-5102 | L1 - Storefront Frames (excl. Main Entry Facade) | 8 | 0 | 02-Sep-14 A | 11-Sep-14 A | |

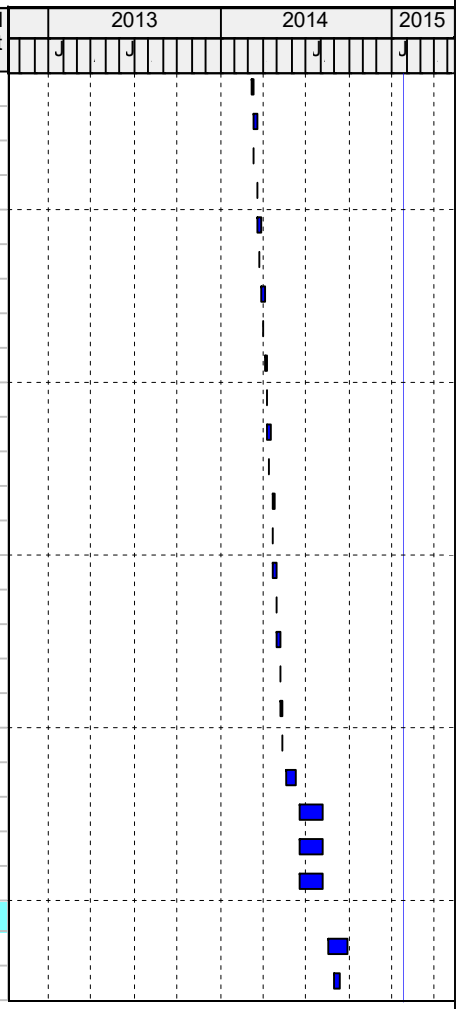


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1-5104 | L1 - Storefront Glazing (excl. Main Entry Facade) | 4 | 0 | 19-Sep-14 A | 24-Sep-14 A | |
| EP-5110 | L1 - Revolving Doors | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L3-5104 | L3 - Storefront Glazing | 3 | 0 | 30-Sep-14 A | 03-Oct-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Levels 3-4** | | | | | | |
| L3-5130 | L3 - Install Punch Windows | 5 | 0 | 24-Feb-14 A | 10-Mar-14 A | |
| L4-5130 | L4 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 12-Mar-14 A | |
| L5-5130 | L5 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L6-5130 | L6- Install Punch Windows | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L7-5130 | L7 - Install Punch Windows | 5 | 0 | 18-Mar-14 A | 21-Mar-14 A | |
| L8-5130 | L8 - Install Punch Windows | 5 | 0 | 24-Mar-14 A | 28-Mar-14 A | |
| L9-5130 | L9 - Install Punch Windows | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L10-5130 | L10 - Install Punch Windows | 5 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-5130 | L11 - Install Punch Windows | 5 | 0 | 14-Apr-14 A | 21-Apr-14 A | |
| L12-5130 | L12 - Install Punch Windows | 5 | 0 | 22-Apr-14 A | 25-Apr-14 A | |
| L14-5130 | L14 - Install Punch Windows | 5 | 0 | 28-Apr-14 A | 05-May-14 A | |
| L15-5130 | L15 - Install Punch Windows | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| L16-5130 | L16 - Install Punch Windows | 5 | 0 | 12-May-14 A | 20-May-14 A | |
| L17-5130 | L17 - Install Punch Windows | 5 | 0 | 27-May-14 A | 16-Jun-14 A | |
| **Roofs** | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| RF-4026 | L1 - City Park - Protection Board | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| **Pool Membrane - (elev 18')** | | | | | | |
| RF-4034 | Pool - Install plumbing | 3 | 0 | 20-Oct-14 A | 22-Oct-14 A | |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |

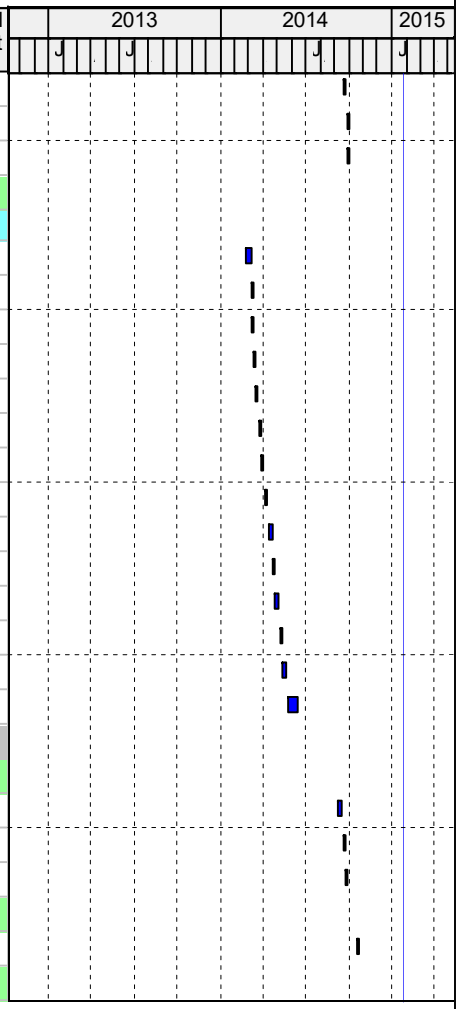



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| RF-4010 | AR - Set Mechanical Equipment | 5 | 0 | 10-Jun-14 A | 12-Jun-14 A | |
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 10 | 0 | 04-Aug-14 A | 27-Aug-14 A | |
| RF-4012 | L2.5 Horseshoe - Install corrugated metal panels | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 8 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |
| PC-4008 | RF - Entry / Porte Cochere Roofing System | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | RF - Upper Ballroom Roofing System | 3 | 0 | 28-Jul-14 A | 31-Jul-14 A | |
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 4 | 0 | 31-Jul-14 A | 04-Aug-14 A | |
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |
| RF-4018 | TR - Terrace Roof - Green Roofing System | 5 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| RF-4020 | TR - Terrace Roof - Install sheet metal capping[DELE | 1 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4022 | TR - Terrace Roof - Install deocrative metal railing | 3 | 3 | 12-Feb-15 | 16-Feb-15 | 39 |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Perimeter Framing / Sul | 10 | 0 | 02-Jun-14 A | 08-Jul-14 A | |
| RF-4002 | Tower Roof - Roofing System | 10 | 0 | 20-Aug-14 A | 17-Sep-14 A | |
| **PH - Roof - (elev 173')** | | | | | | |
| RF-4030 | PH - Roofing System | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| RF-4032 | PH - Coping / Flashing [DELETED] | 3 | 0 | 01-Sep-14 A | 01-Sep-14 A | |
| **Rough-In's** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6002 | LL4 - Layout | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| LL4-6008 | LL4 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL4-6012 | LL4 - Fire Sprinkler Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |

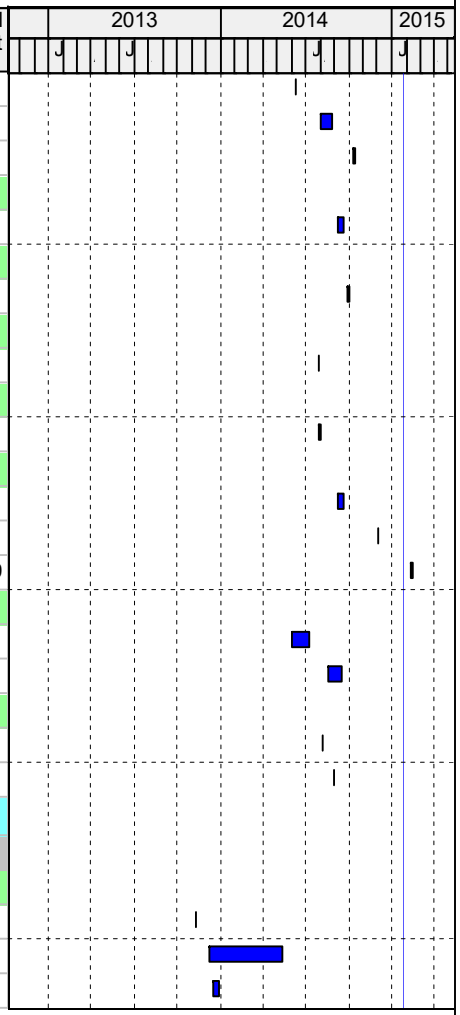


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-6014 | LL4 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6018 | LL4 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6004 | LL4 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL4-6016 | LL4 - Electrical RI | 10 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties RI | 8 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6010 | LL4 - Elevator pits | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| LL4-6020 | LL4 - H Mtl Frames | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL4-6024 | LL4 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6002 | LL3 - Layout | 1 | 0 | 19-Nov-13 A | 19-Nov-13 A | |
| LL3-6008 | LL3 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL3-6012 | LL3 - Fire Sprinkler RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6014 | LL3 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6018 | LL3 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6004 | LL3 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL3-6020 | LL3 - H Mtl Frames | 3 | 0 | 08-May-14 A | 09-May-14 A | |
| LL3-6010 | LL3 - F/P Curbs | 5 | 0 | 19-May-14 A | 19-May-14 A | |
| LL3-6016 | LL3 - Electrical RI | 2 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties RI | 8 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL3-6024 | LL3 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6002 | LL2 - Layout | 1 | 0 | 14-Jan-14 A | 14-Jan-14 A | |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| LL2-6012 | LL2 - Fire Sprinkler RI | 10 | 0 | 21-Jan-14 A | 03-Feb-14 A | |
| LL2-6014 | LL2 - Plumbing RI | 10 | 0 | 21-Jan-14 A | 14-Feb-14 A | |

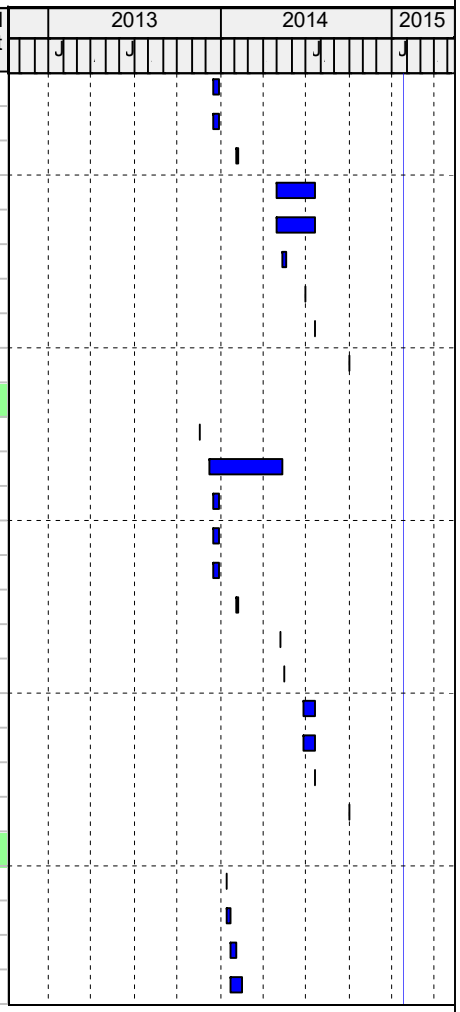



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2E-6016 | LL2 - Electrical RI | 8 | 0 | 03-Feb-14 A | 17-Mar-14 A | |
| LL2-6016 | LL2 - Electrical RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2-6018 | LL2 - HVAC RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2–6004 | LL2 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL2E-6004 | LL2 - CMU Walls | 10 | 0 | 04-Mar-14 A | 09-May-14 A | |
| LL2E-6012 | LL2 - Fire Sprinkler RI | 8 | 0 | 21-Mar-14 A | 01-Apr-14 A | |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 24-Apr-14 A | |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 3 | 0 | 23-Apr-14 A | 21-Jul-14 A | |
| LL2E-6020 | LL2 - H Mtl Frames | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| LL2-6020 | LL2 - H Mtl Frames | 3 | 0 | 12-May-14 A | 13-May-14 A | |
| LL2E-6008 | LL2 - Int Wall Framing | 5 | 0 | 13-May-14 A | 22-Jun-14 A | |
| LL2E-6014 | LL2 - Plumbing RI | 8 | 0 | 13-May-14 A | 30-May-14 A | |
| LL2E-6018 | LL2 - HVAC RI | 8 | 0 | 13-May-14 A | 04-Aug-14 A | |
| LL2E-6022 | LL2 - Fire Alarm / Elec Specialties RI (East of 10) | 8 | 0 | 13-May-14 A | 22-Sep-14 A | |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties RI (West of 10) | 8 | 0 | 19-May-14 A | 22-Sep-14 A | |
| LL2-6015 | LL2 - Main Elect Room Set Equip / RI - Power to Ma | 15 | 0 | 30-Jun-14 A | 26-Sep-14 A | |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 0 | 16-Jul-14 A | 21-Jul-14 A | |
| LL2-6024 | LL2 - Inspections | 2 | 0 | 15-Sep-14 A | 03-Oct-14 A | |
| LL2-6010 | F/P Curbs at Garage | 5 | 5 | 02-Mar-15 | 06-Mar-15 | 21 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6002 | Layout | 3 | 0 | 03-Jan-14 A | 08-Jan-14 A | |
| LL1-6008 | Int Wall Framing & Inspection | 6 | 0 | 08-Jan-14 A | 21-Jul-14 A | |
| LL1-Z2-6002 | Layout | 3 | 0 | 08-Jan-14 A | 14-Jan-14 A | |
| LL1-Z3-6002 | Layout | 3 | 0 | 14-Jan-14 A | 17-Jan-14 A | |
| LL1-Z2-6008 | Int Wall Framing & Inspection | 6 | 0 | 17-Jan-14 A | 01-Aug-14 A | |
| LL1-Z3-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-Jan-14 A | 04-Aug-14 A | |

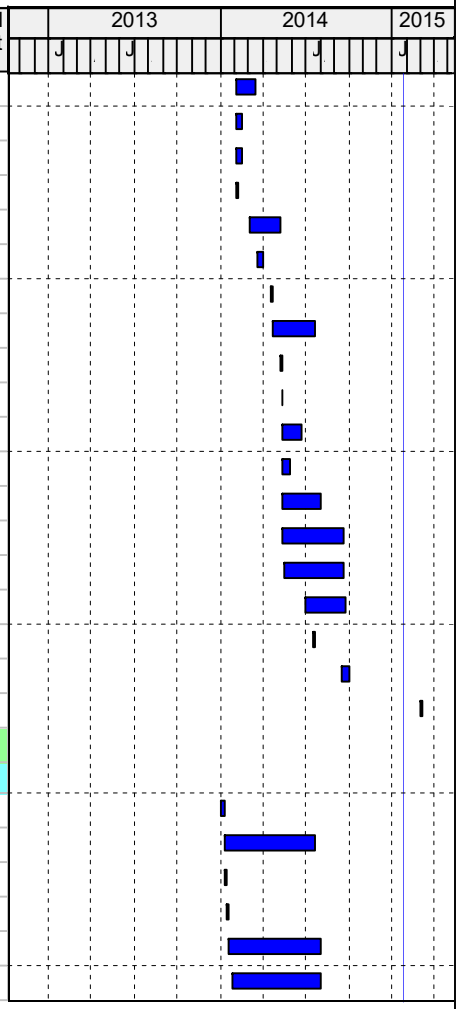


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 09-May-14 A | |
| LL1-Z2-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 28-Apr-14 A | |
| LL1-Z3-6004 | CMU Walls (At All Areas North of Q-Line) | 3 | 0 | 03-Feb-14 A | 13-May-14 A | |
| LL1C-6012 | Complete Fire Sprinkler RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6016 | Complete Electrical RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 10 | 0 | 17-Feb-14 A | 16-Sep-14 A | |
| LL1C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 30-Apr-14 A | |
| LL1-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-Z2-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z2-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z3-6012 | Fire Sprinkler RI (At All Areas North of Q-Line) | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z3-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 11-Sep-14 A | |
| LL1-Z3-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z2C-6012 | Complete Fire Sprinkler RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6014 | Complete Plumbing RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6016 | Complete Electrical RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 15 | 0 | 24-Feb-14 A | 15-Sep-14 A | |
| LL1-Z2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |

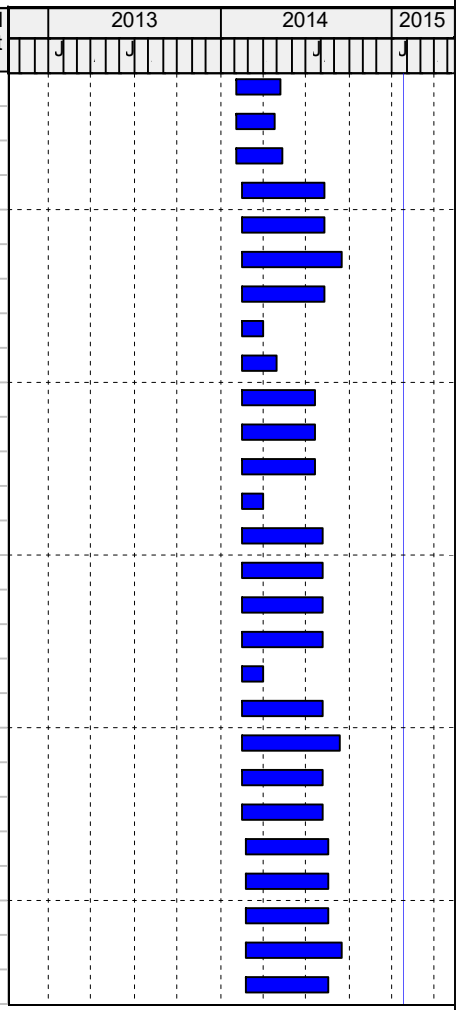


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-6020 | Hollow Metal Door Frames | 5 | 0 | 17-Mar-14 A | 04-Apr-14 A | |
| LL1-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| LL1-Z3-6020 | Hollow Metal Door Frames (At All Areas North of Q-Lir | 1 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| L1B-6004 | CMU Walls [including East Service Corridor] | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L1L-6002 | Layout [including back of house] | 3 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 29-Apr-14 A | |
| L1B-6008 | Int Wall Framing & Inspection | 6 | 0 | 21-Apr-14 A | 08-Aug-14 A | |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 5 | 0 | 25-Apr-14 A | 21-Jul-14 A | |
| LL1C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L1K-6004 | CMU Walls [including public restroom] | 3 | 0 | 05-May-14 A | 08-May-14 A | |
| L1K-6002 | Layout [including public restroom] | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| L1K-6008 | Int Wall Framing & Inspection | 4 | 0 | 09-May-14 A | 22-Aug-14 A | |
| L1B-6002 | Layout [including East Service Corridor] | 3 | 0 | 14-May-14 A | 27-May-14 A | |
| L1L-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-May-14 A | 06-Oct-14 A | |
| L1L-6004 | CMU Walls [including back of house] | 3 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L1K-6012 | Fire Sprinkler RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6014 | Plumbing RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6016 | Electrical RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1K-6018 | HVAC RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1B-6014 | Plumbing RI [including East Service Corridor] | 10 | 0 | 16-Jun-14 A | 24-Jun-14 A | |
| L1B-6018 | HVAC RI | 10 | 0 | 20-Jun-14 A | 15-Aug-14 A | |
| L1B-6012 | Fire Sprinkler RI | 10 | 0 | 21-Jun-14 A | 15-Aug-14 A | |
| L1L-6018 | HVAC RI | 5 | 0 | 23-Jun-14 A | 13-Oct-14 A | |
| L1L-6014 | Plumbing RI | 5 | 0 | 24-Jun-14 A | 28-Oct-14 A | |
| L1L-6010 | CMU Seismic Clips [including back of house] [DELETI | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1L-6012 | Fire Sprinkler RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |
| L1L-6016 | Electrical RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |

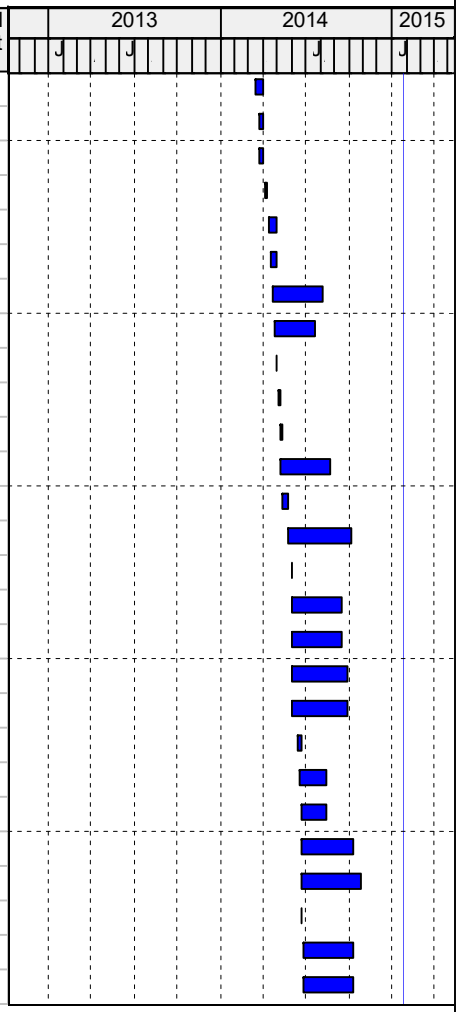


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 27-Jun-14 A | 13-Oct-14 A | |
| L1K-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 27-Jun-14 A | 29-Sep-14 A | |
| LL1-Z3-6009 | Frame Ceilings [DELETED] | 4 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1B-6016 | Electrical RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| L1B-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| LL1-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-Z2-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L1B-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-6024 | Inspections for Cover | 1 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L1B-6020 | Hollow Metal Door Frames | 5 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| LL1-Z3-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L1K-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 06-Aug-14 A | |
| LL1-Z2-6024 | Inspections for Cover | 2 | 0 | 07-Aug-14 A | 08-Aug-14 A | |
| L1K-6020 | Hollow Metal Door Frames | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-Z2-6009 | Frame Ceilings & Inspection | 6 | 0 | 22-Aug-14 A | 13-Oct-14 A | |
| L1L-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Aug-14 A | 13-Oct-14 A | |
| LL1-6009 | Frame Ceilings & Inspection (except for bar redesign | 9 | 0 | 02-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3-6024 | Inspections for Cover | 2 | 0 | 12-Sep-14 A | 12-Sep-14 A | |
| LL1-Z3C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6016 | Complete Electrical RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3C-6018 | Complete HVAC RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| L1KC-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 4 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L1B-6024 | Inspections for Cover (Main Ballroom N/S/W Walls & | 3 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1K-6024 | Inspections for Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1KC-6014 | Complete Plumbing RI @ Ceilings & Inspection | 4 | 0 | 02-Oct-14 A | 07-Oct-14 A | |

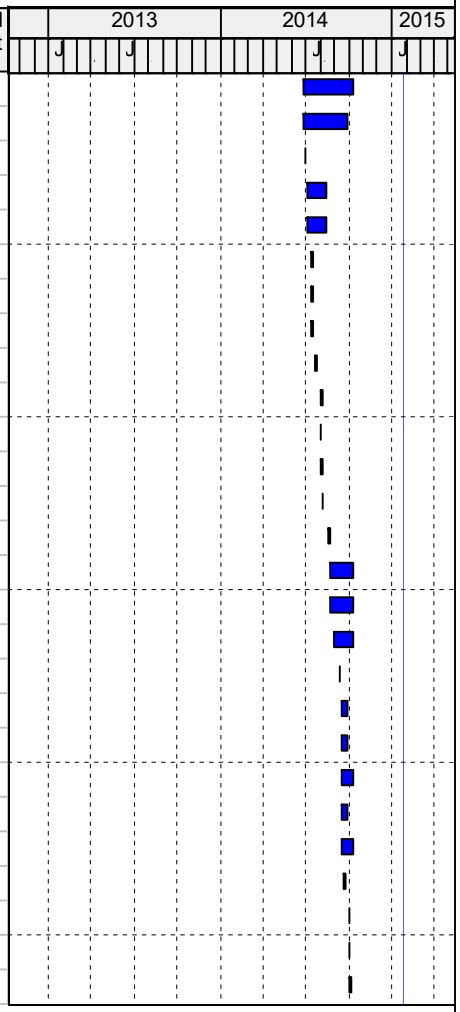


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1BC-6014 | Complete Plumbing RI @ Ceilings | 7 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L1KC-6018 | Complete HVAC RI @ Ceilings & Inspection | 4 | 0 | 06-Oct-14 A | 10-Nov-14 A | |
| L1KC-6016 | Complete Electrical RI @ Ceilings & Inspection | 3 | 0 | 20-Oct-14 A | 10-Nov-14 A | |
| L1KC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 3 | 0 | 20-Oct-14 A | 10-Nov-14 A | |
| L1L-6024 | Inspections for Cover | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L1L-6009 | Frame ceilings & inspection at high ceiling | 13 | 0 | 24-Nov-14 A | 20-Jan-15 A | |
| L1B-6009 | Frame Ceilings & inspection at Main Ballroom (per rev | 5 | 0 | 04-Dec-14 A | 16-Jan-15 A | |
| L1LC-6012 | Complete fire sprinkler RI @ ceilings | 5 | 1 | 05-Jan-15 A | 26-Jan-15 | 0 |
| L1LC-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| L1LC-6016 | Complete electrical rough-in @ ceilings & inspection | 5 | 1 | 05-Jan-15 A | 26-Jan-15 | 0 |
| L1LC-6018 | Complete HVAC RI @ Ceilings | 5 | 1 | 05-Jan-15 A | 26-Jan-15 | 0 |
| L1LC-6022 | Complete fire alarm/elec specialties RI @ ceilings & ir | 5 | 1 | 05-Jan-15 A | 26-Jan-15 | 0 |
| L1K-6009 | Frame ceilings & inspection at public restroom | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L1B-8118 | Lighting & electrical trim at Ballrooms | 5 | 5 | 18-Mar-15 | 24-Mar-15 | 0 |
| L1B-8204 | HVAC trim at Ballrooms | 5 | 5 | 18-Mar-15 | 24-Mar-15 | 0 |
| L1B-8112 | Fire sprinkler trim at Ballrooms | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 3 |
| L1BC-6022 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 3 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 0 | 17-Apr-14 A | 09-May-14 A | |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6006 | L2 - Support Frame/Sheathing for Metal Panels | 6 | 0 | 23-Apr-14 A | 07-Aug-14 A | |
| L02-6008 | L2 - Int Wall Framing | 10 | 0 | 25-Apr-14 A | 17-Jul-14 A | |
| L02-6014 | L2 - Plumbing RI | 15 | 0 | 28-Apr-14 A | 07-Aug-14 A | |
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 0 | 28-Apr-14 A | 09-May-14 A | |
| L02-6004 | L2 - CMU Walls | 5 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L02-6002 | L2 - Layout | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 0 | 19-May-14 A | 19-May-14 A | |

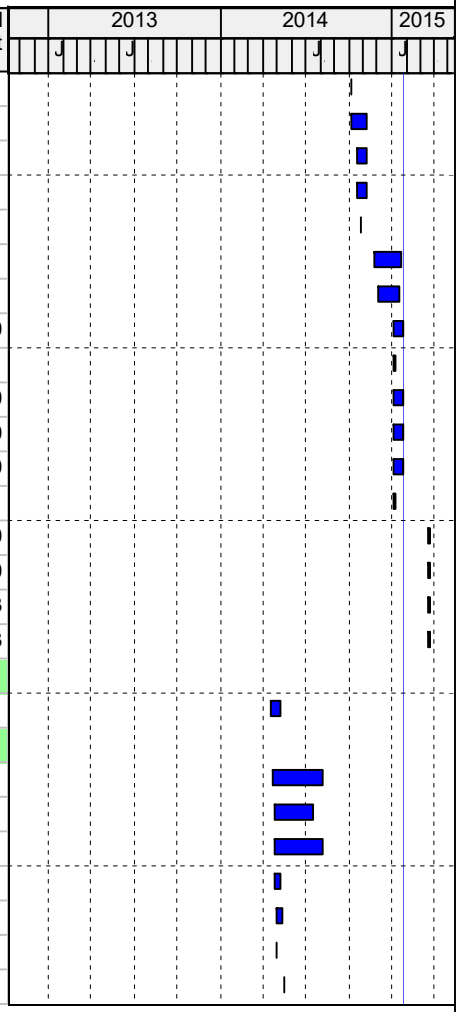


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-6018 | L2 - HVAC RI (including equipment) | 20 | 0 | 18-Jun-14 A | 10-Sep-14 A | |
| L02-6016 | L2 - Electrical RI | 10 | 0 | 24-Jun-14 A | 14-Aug-14 A | |
| L02-6022 | L2 - Fire Alarm / Elec Specialties RI | 10 | 0 | 24-Jun-14 A | 10-Oct-14 A | |
| L02-6012 | L2 - Fire Sprinkler RI | 10 | 0 | 26-Jun-14 A | 07-Aug-14 A | |
| L02-6020 | L2 - H Mtl Frames | 5 | 0 | 11-Jul-14 A | 17-Jul-14 A | |
| L02-6024 | L2 - Inspections - North Half | 2 | 0 | 10-Oct-14 A | 20-Oct-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L07-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 01-Apr-11 A | 11-Apr-11 A | |
| L04-6012 | Fire Sprinkler Mains | 5 | 0 | 01-Feb-14 A | 03-Apr-14 A | |
| L03-8219 | HVAC Risers | 5 | 0 | 11-Feb-14 A | 23-Mar-14 A | |
| L03-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 11-Feb-14 A | 03-Mar-14 A | |
| L03-6002 | Layout | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| L04-8219 | HVAC Risers | 5 | 0 | 13-Feb-14 A | 23-Mar-14 A | |
| L05-8219 | HVAC Risers | 5 | 0 | 17-Feb-14 A | 03-Mar-14 A | |
| L03-6008 | Frame Shaft Walls | 3 | 0 | 18-Feb-14 A | 26-Mar-14 A | |
| L04-6002 | Layout | 5 | 0 | 19-Feb-14 A | 25-Feb-14 A | |
| L04-6008 | Frame Shaft Walls | 3 | 0 | 20-Feb-14 A | 26-Mar-14 A | |
| L03-6011 | PreRock Shafts | 2 | 0 | 24-Feb-14 A | 25-Mar-14 A | |
| L03-6010 | Frame Walls | 5 | 0 | 25-Feb-14 A | 25-Mar-14 A | |
| L05-6002 | Layout | 5 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| L04-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 28-Feb-14 A | 05-Mar-14 A | |
| L03-6016 | Electrical RI | 5 | 0 | 03-Mar-14 A | 04-Apr-14 A | |
| L03-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 12-Mar-14 A | |
| L04-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 13-Mar-14 A | |
| L04-6010 | Frame Walls | 5 | 0 | 04-Mar-14 A | 05-Jun-14 A | |
| L05-6008 | Frame Shaft Walls | 3 | 0 | 05-Mar-14 A | 27-Mar-14 A | |

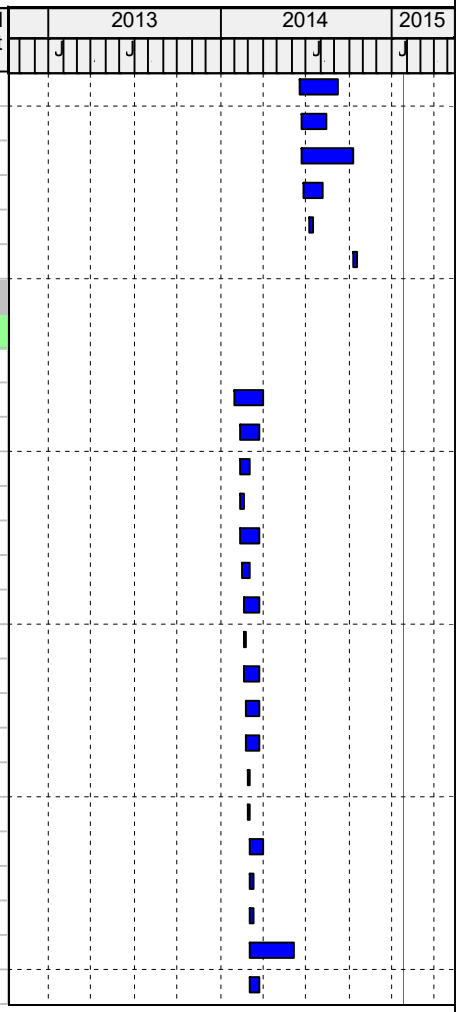



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L07-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L05-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 06-Mar-14 A | 21-Mar-14 A | |
| L03-6020 | Install Hollow Metal Frames | 3 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L04-6020 | Install Hollow Metal Frames | 3 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L05-6010 | Frame Walls | 5 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L06-6002 | Layout | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L04-6011 | PreRock Shafts | 2 | 0 | 18-Mar-14 A | 25-Mar-14 A | |
| L05-6009 | Inspect Shafts | 1 | 0 | 18-Mar-14 A | 18-Mar-14 A | |
| L05-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| L06-6008 | Frame Shaft Walls | 3 | 0 | 19-Mar-14 A | 03-Apr-14 A | |
| L06-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 27-Mar-14 A | |
| L04-6016 | Electrical RI | 5 | 0 | 20-Mar-14 A | 09-Apr-14 A | |
| L05-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 26-Mar-14 A | |
| L06-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 07-Apr-14 A | |
| L07-6002 | Layout | 5 | 0 | 24-Mar-14 A | 30-Apr-14 A | |
| L03-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L03-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L05-6016 | Electrical RI | 5 | 0 | 25-Mar-14 A | 05-Jun-14 A | |
| L04-6019 | Complete Top Out GWB | 2 | 0 | 26-Mar-14 A | 06-Jun-14 A | |
| L05-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L06-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| L03-6019 | Complete Top Out GWB | 2 | 0 | 27-Mar-14 A | 02-May-14 A | |
| L08-6002 | Layout | 5 | 0 | 27-Mar-14 A | 02-Apr-14 A | |
| L05-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 28-Mar-14 A | 03-Apr-14 A | |

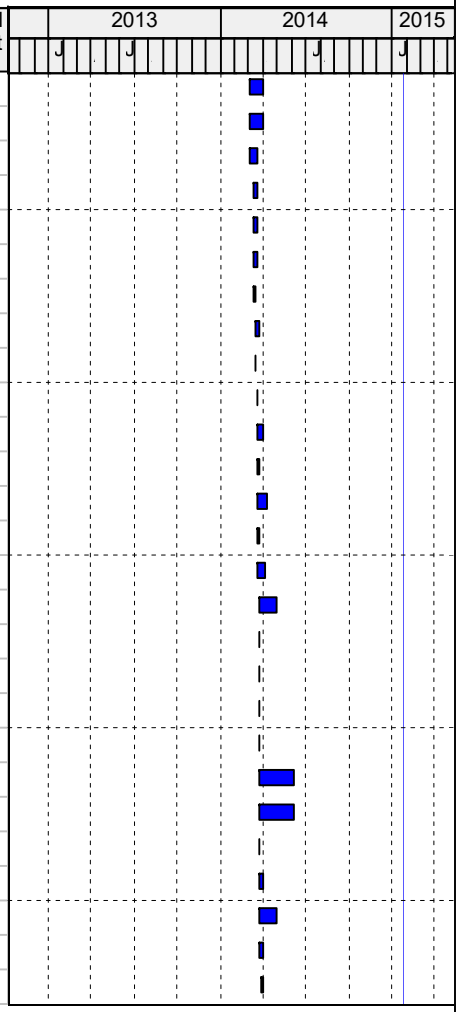


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-6010 | Frame Walls | 5 | 0 | 28-Mar-14 A | 07-Apr-14 A | |
| L03-6012 | Fire Sprinkler Mains | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L07-6008 | Frame Shaft Walls | 3 | 0 | 31-Mar-14 A | 03-Apr-14 A | |
| L05-6019 | Complete Top Out GWB | 2 | 0 | 01-Apr-14 A | 08-Apr-14 A | |
| L08-6008 | Frame Shaft Walls | 3 | 0 | 02-Apr-14 A | 21-Apr-14 A | |
| L03-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L04-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L05-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L06-6016 | Electrical RI | 5 | 0 | 03-Apr-14 A | 15-Apr-14 A | |
| L07-6009 | Inspect Shafts | 1 | 0 | 03-Apr-14 A | 03-Apr-14 A | |
| L07-6011 | PreRock Shafts | 2 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| L05-6012 | Fire Sprinkler Mains | 5 | 0 | 04-Apr-14 A | 30-Apr-14 A | |
| L06-6012 | Fire Sprinkler Mains | 5 | 0 | 07-Apr-14 A | 30-Apr-14 A | |
| L06-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L06-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L07-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| L07-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L03-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L03-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L04-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L06-6009 | Inspect Shafts | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L06-6019 | Complete Top Out GWB | 2 | 0 | 08-Apr-14 A | 18-Apr-14 A | |
| L07-6010 | Frame Walls | 5 | 0 | 08-Apr-14 A | 15-Apr-14 A | |
| L08-6011 | PreRock Shafts | 2 | 0 | 08-Apr-14 A | 23-Apr-14 A | |
| L09-6002 | Layout | 5 | 0 | 08-Apr-14 A | 26-Apr-14 A | |
| L03-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 09-Apr-14 A | 08-May-14 A | |
| L03-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |

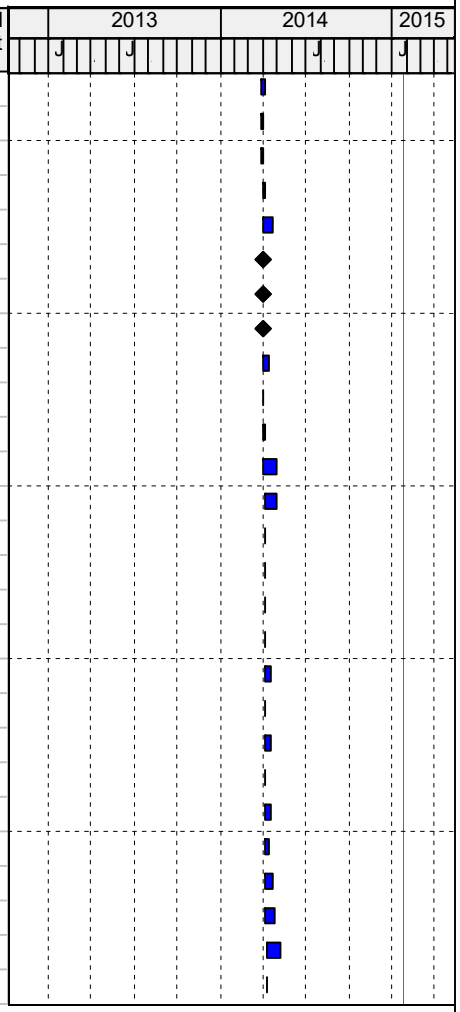



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 09-Apr-14 A | 14-Apr-14 A | |
| L08-6009 | Inspect Shafts | 1 | 0 | 09-Apr-14 A | 25-Apr-14 A | |
| L09-6008 | Frame Shaft Walls | 3 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| L08-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| L04-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 15-Apr-14 A | 16-Apr-14 A | |
| L07-6012 | Fire Sprinkler Mains | 5 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| L07-6016 | Electrical RI | 5 | 0 | 15-Apr-14 A | 12-May-14 A | |
| L07-6020 | Install Hollow Metal Frames | 3 | 0 | 16-Apr-14 A | 23-Apr-14 A | |
| L05-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 17-Apr-14 A | 25-Apr-14 A | |
| L06-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 17-Apr-14 A | 12-May-14 A | |
| L06-6023 | Inspection of Exterior Framing | 0 | 0 | 17-Apr-14 A | | |
| L09-8219 | HVAC Risers | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L09-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L04-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 18-Apr-14 A | 20-Apr-14 A | |
| L04-6028 | PreRock at Heat Pumps | 2 | 0 | 20-Apr-14 A | 22-Apr-14 A | |
| L08-8219 | HVAC Risers | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6009 | Inspect Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6011 | PreRock Shafts | 2 | 0 | 22-Apr-14 A | 24-Apr-14 A | |
| L04-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L06-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 23-Apr-14 A | 25-Apr-14 A | |
| L08-6020 | Install Hollow Metal Frames | 3 | 0 | 23-Apr-14 A | 13-May-14 A | |
| L11-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L11-8220 | Plumbing Risers - Install | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L04-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L09-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |

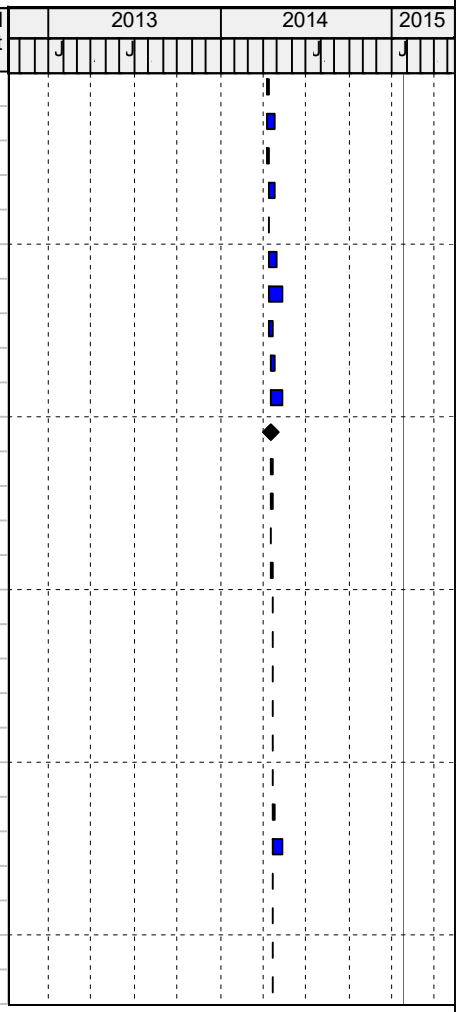


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L10-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 20-May-14 A | |
| L12-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L04-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 25-Apr-14 A | 11-Jun-14 A | |
| L04-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L09-6010 | Frame Walls | 5 | 0 | 25-Apr-14 A | 20-May-14 A | |
| L09-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L10-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L11-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 30-Apr-14 A | |
| L12-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L08-6010 | Frame Walls | 5 | 0 | 26-Apr-14 A | 30-Apr-14 A | |
| L10-6002 | Layout | 5 | 0 | 27-Apr-14 A | 27-Apr-14 A | |
| L04-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 28-Apr-14 A | 30-Apr-14 A | |
| L05-6018 | HVAC RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6028 | PreRock at Heat Pumps | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L07-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 28-Apr-14 A | 12-May-14 A | |
| L10-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-Apr-14 A | 22-May-14 A | |
| L11-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L12-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L05-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| L05-6028 | PreRock at Heat Pumps | 2 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |

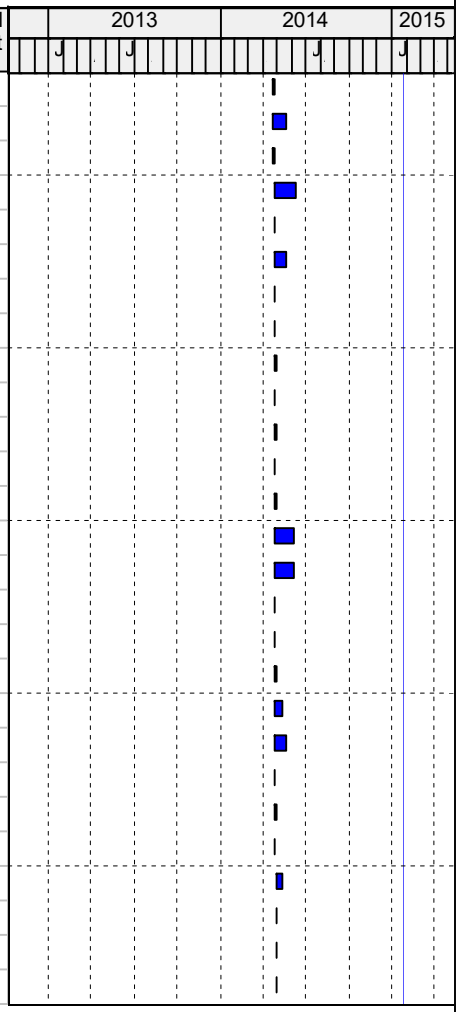



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 09-May-14 A | |
| L06-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L06-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L08-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L08-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L09-6020 | Install Hollow Metal Frames | 3 | 0 | 29-Apr-14 A | 20-May-14 A | |
| L09-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L10-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L04-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 30-Apr-14 A | 02-May-14 A | |
| L09-6019 | Complete Top Out GWB | 2 | 0 | 30-Apr-14 A | 06-Jun-14 A | |
| L11-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L12-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L03-6028 | PreRock at Heat Pumps | 2 | 0 | 01-May-14 A | 02-May-14 A | |
| L05-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L06-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L03-6014 | Set Tubs & Plumbing RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L05-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L05-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| L06-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L06-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 09-May-14 A | |
| L03-6018 | HVAC RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L03-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 06-May-14 A | 06-May-14 A | |
| L07-6014 | Set Tubs & Plumbing RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |

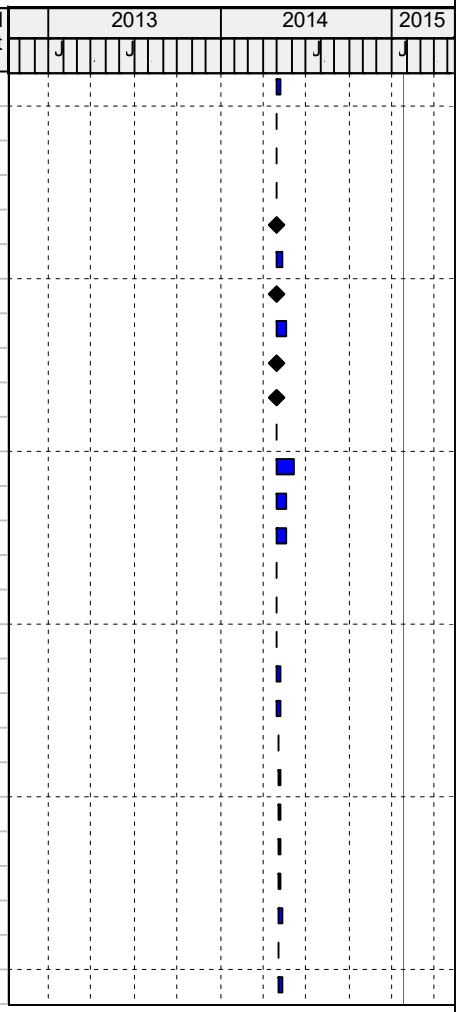


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 06-May-14 A | 09-May-14 A | |
| L03-6004 | CMU Wall/Clips | 3 | 0 | 07-May-14 A | 08-May-14 A | |
| L03-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L03-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 08-May-14 A | 13-May-14 A | |
| L03-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6004 | CMU Walls | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6018 | HVAC RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L11-6010 | Frame Walls | 5 | 0 | 09-May-14 A | 15-May-14 A | |
| L05-6014 | Set Tubs & Plumbing RI | 5 | 0 | 12-May-14 A | 05-Jun-14 A | |
| L07-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 0 | 12-May-14 A | 13-May-14 A | |
| L11-6020 | Install Hollow Metal Frames | 3 | 0 | 12-May-14 A | 14-May-14 A | |
| L11-6019 | Complete Top Out GWB | 2 | 0 | 12-May-14 A | 14-May-14 A | |
| L14-6002 | Layout | 5 | 0 | 12-May-14 A | 14-May-14 A | |
| L15-6002 | Layout | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L05-6004 | CMU Walls | 3 | 0 | 13-May-14 A | 13-May-14 A | |
| L06-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 25-Jun-14 A | |
| L06-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 13-May-14 A | 14-Jul-14 A | |
| L07-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 05-Jun-14 A | |
| L07-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| L07-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 13-May-14 A | 13-May-14 A | |
| L14-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L16-6002 | Layout | 5 | 0 | 13-May-14 A | 16-May-14 A | |
| L06-6004 | CMU Walls | 3 | 0 | 14-May-14 A | 14-May-14 A | |
| L07-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 15-May-14 A | |

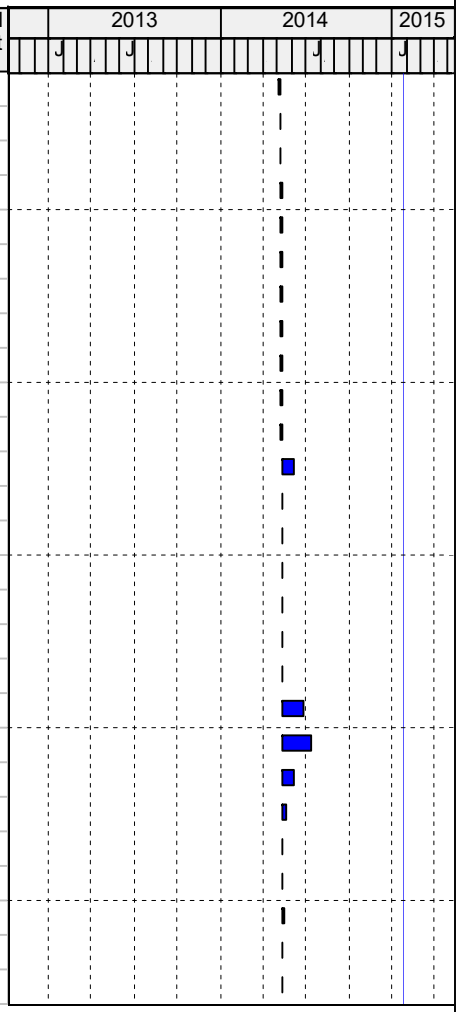



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-6012 | Fire Sprinkler Mains | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6002 | Layout | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L07-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6014 | Set Tubs & Plumbing RI | 5 | 0 | 16-May-14 A | 25-Jun-14 A | |
| L08-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L11-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L12-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L07-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L08-6028 | PreRock at Heat Pumps | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L09-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L10-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L11-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L15-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 19-May-14 A | 19-May-14 A | |
| L07-6028 | PreRock at Heat Pumps | 2 | 0 | 20-May-14 A | 21-May-14 A | |
| L07-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L08-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 20-May-14 A | 21-May-14 A | |
| L10-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L11-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L14-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L07-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 21-May-14 A | 27-May-14 A | |
| L08-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 21-May-14 A | 21-May-14 A | |

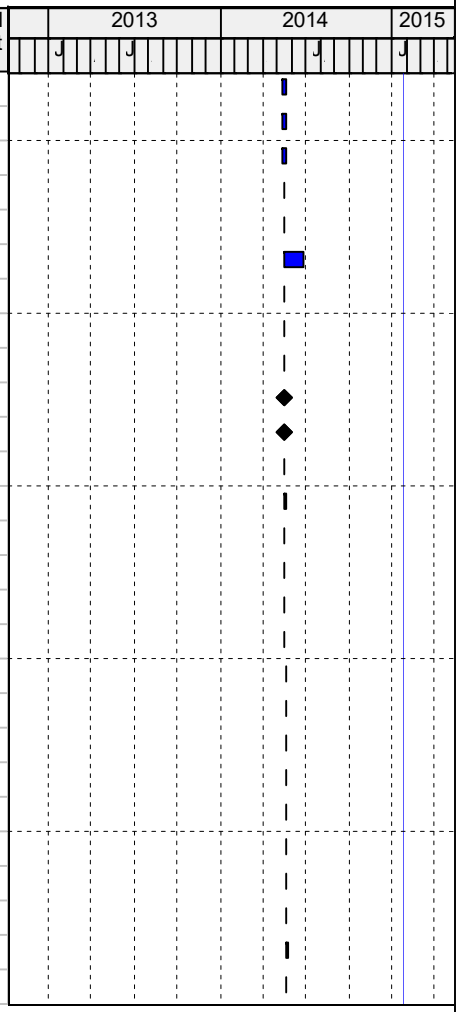


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L09-6028 | PreRock at Heat Pumps | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L10-6014 | Set Tubs & Plumbing RI | 5 | 0 | 21-May-14 A | 27-Jun-14 A | |
| L10-6010 | Frame Walls | 5 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6019 | Complete Top Out GWB | 2 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L11-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L12-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L14-8220 | Plumbing Risers - Install | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L15-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L16-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L07-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| L08-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 22-May-14 A | 22-May-14 A | |
| L10-6012 | Fire Sprinkler Mains | 5 | 0 | 22-May-14 A | 27-May-14 A | |
| L08-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L09-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6020 | Install Hollow Metal Frames | 3 | 0 | 23-May-14 A | 03-Jun-14 A | |
| L10-6028 | PreRock at Heat Pumps | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L14-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L15-8220 | Plumbing Risers - Install | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L09-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 27-May-14 A | 27-May-14 A | |
| L12-6010 | Frame Walls | 5 | 0 | 27-May-14 A | 02-Jun-14 A | |
| L08-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L09-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 28-May-14 A | 28-May-14 A | |
| L10-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 28-May-14 A | 03-Jun-14 A | |
| L14-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L15-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-May-14 A | 30-May-14 A | |

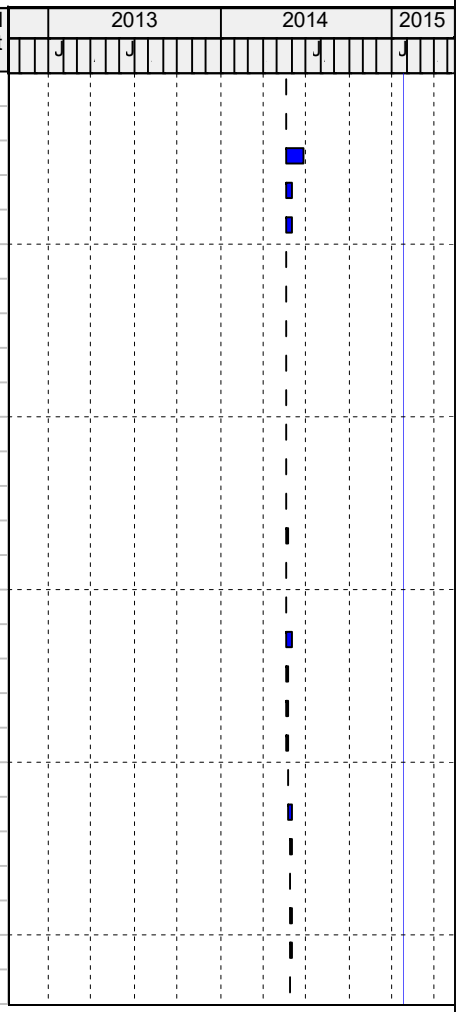



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 28-May-14 A | 28-May-14 A | |
| L16-8220 | Plumbing Risers - Install | 2 | 0 | 28-May-14 A | 29-May-14 A | |
| L08-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 29-May-14 A | 30-May-14 A | |
| L10-6016 | Electrical RI | 5 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L10-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| L12-6012 | Fire Sprinkler Mains | 5 | 0 | 30-May-14 A | 26-Jun-14 A | |
| L12-6020 | Install Hollow Metal Frames | 3 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L15-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L17-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L17-8220 | Plumbing Risers - Install | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L10-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L11-6016 | Electrical RI | 5 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L11-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L12-6019 | Complete Top Out GWB | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L14-6020 | Install Hollow Metal Frames | 3 | 0 | 02-Jun-14 A | 05-Jun-14 A | |
| L14-6010 | Frame Walls | 5 | 0 | 02-Jun-14 A | 04-Jun-14 A | |
| L16-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| L14-6019 | Complete Top Out GWB | 2 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L16-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L10-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| L17-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 04-Jun-14 A | 11-Jun-14 A | |
| L08-6016 | Electrical RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L08-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L09-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L12-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |

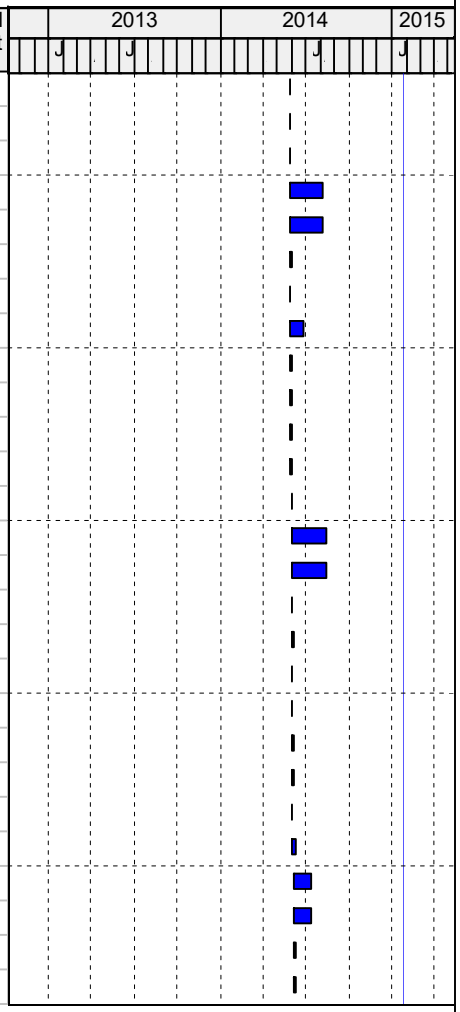


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6010 | Frame Walls | 3 | 0 | 05-Jun-14 A | 11-Jun-14 A | |
| L09-6012 | Fire Sprinkler Mains | 5 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L09-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L11-6012 | Fire Sprinkler Mains | 4 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L12-6014 | Set Tubs & Plumbing RI | 4 | 0 | 06-Jun-14 A | 27-Jun-14 A | |
| L11-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jun-14 A | 11-Jun-14 A | |
| L09-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-Jun-14 A | 25-Jun-14 A | |
| L14-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L15-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L16-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L09-6016 | Electrical RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L14-6014 | Set Tubs & Plumbing RI | 4 | 0 | 10-Jun-14 A | 21-Jul-14 A | |
| L15-6020 | Install Hollow Metal Frames | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L15-6019 | Complete Top Out GWB | 2 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6014 | Set Tubs & Plumbing RI | 4 | 0 | 11-Jun-14 A | 26-Jun-14 A | |
| L11-6028 | PreRock at Heat Pumps | 2 | 0 | 13-Jun-14 A | 14-Jun-14 A | |
| L11-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 14-Jun-14 A | 14-Jun-14 A | |
| L14-6012 | Fire Sprinkler Mains | 2 | 0 | 16-Jun-14 A | 27-Jun-14 A | |
| L14-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 0 | 18-Jun-14 A | 18-Jun-14 A | |
| L15-6023 | Inspection of Exterior Framing | 0 | 0 | 18-Jun-14 A | | |
| L17-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 18-Jun-14 A | 23-Jun-14 A | |
| L17-6010 | Frame Walls | 5 | 0 | 18-Jun-14 A | 29-Jul-14 A | |
| L10-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L12-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 20-Jun-14 A | |

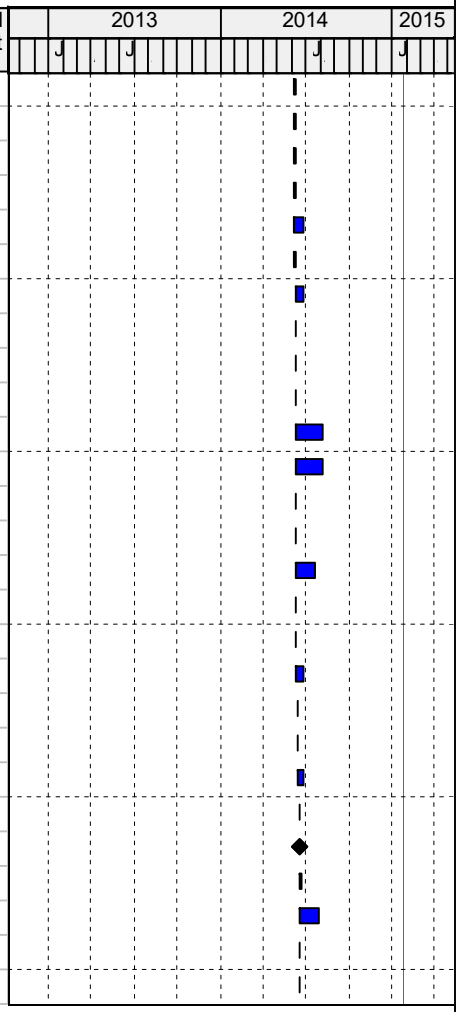



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6023 | Inspection of Exterior Framing | 0 | 0 | 20-Jun-14 A | | |
| L15-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 0 | 20-Jun-14 A | 20-Jun-14 A | |
| L10-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-Jun-14 A | 23-Jun-14 A | |
| L15-6014 | Set Tubs & Plumbing RI | 5 | 0 | 22-Jun-14 A | 24-Jul-14 A | |
| L08-6018 | HVAC RI | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L12-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L14-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L15-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L08-6221 | Frame Unit Ceilings | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| L11-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 24-Jun-14 A | 27-Jun-14 A | |
| L12-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L14-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6023 | Inspection of Exterior Framing | 0 | 0 | 24-Jun-14 A | | |
| L12-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| L12-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L14-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L15-6012 | Fire Sprinkler Mains | 2 | 0 | 25-Jun-14 A | 22-Jul-14 A | |
| L16-6023 | Inspection of Exterior Framing | 0 | 0 | 25-Jun-14 A | | |
| L03-6024 | Inspections for GWB Cover | 1 | 0 | 27-Jun-14 A | 27-Jun-14 A | |
| L09-6018 | HVAC RI | 3 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L09-6221 | Frame Unit Ceilings | 2 | 0 | 27-Jun-14 A | 30-Jun-14 A | |
| L12-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L14-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L15-6028 | PreRock at Heat Pumps | 2 | 0 | 30-Jun-14 A | 01-Jul-14 A | |

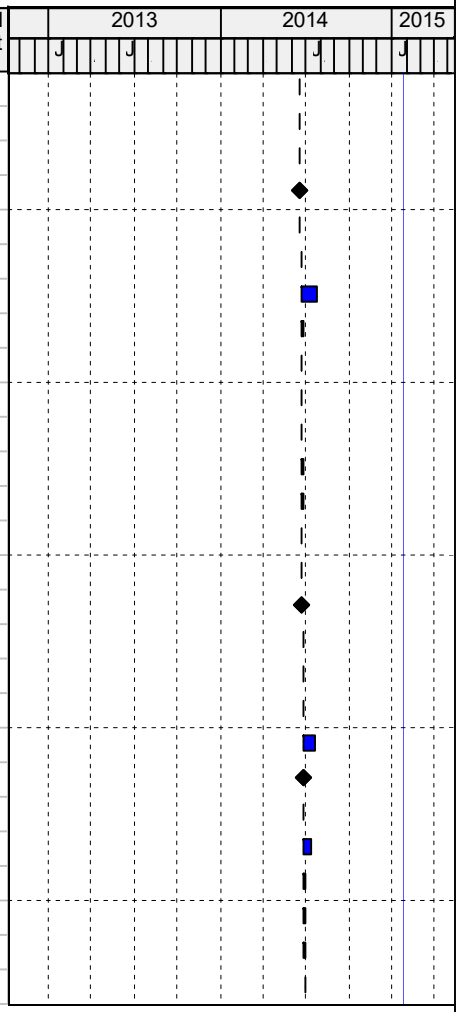



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 30-Jun-14 A | 30-Jun-14 A | |
| L16-6010 | Frame Walls | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| L16-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L15-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L15-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L04-6024 | Inspections for GWB Cover | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L10-6018 | HVAC RI | 3 | 0 | 07-Jul-14 A | 21-Jul-14 A | |
| L11-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L15-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L16-6012 | Fire Sprinkler Mains | 2 | 0 | 07-Jul-14 A | 24-Jul-14 A | |
| L16-6020 | Install Hollow Metal Frames | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L16-6028 | PreRock at Heat Pumps | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L17-6019 | Complete Top Out GWB | 1 | 0 | 07-Jul-14 A | 08-Aug-14 A | |
| L11-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L15-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 08-Jul-14 A | 04-Aug-14 A | |
| L17-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jul-14 A | 01-Aug-14 A | |
| L10-6221 | Frame Unit Ceilings | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| L17-6012 | Fire Sprinkler Mains | 2 | 0 | 09-Jul-14 A | 12-Aug-14 A | |
| L05-6024 | Inspections for GWB Cover | 2 | 0 | 10-Jul-14 A | 10-Jul-14 A | |
| L04-6000 | Tape/Finish GWB | 6 | 0 | 11-Jul-14 A | 23-Jul-14 A | |
| L16-6019 | Complete Top Out GWB | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L16-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L15-6018 | HVAC RI | 3 | 0 | 16-Jul-14 A | 18-Jul-14 A | |
| L16-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-6024 | Inspections for GWB Cover | 2 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6018 | HVAC RI | 3 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L16-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |

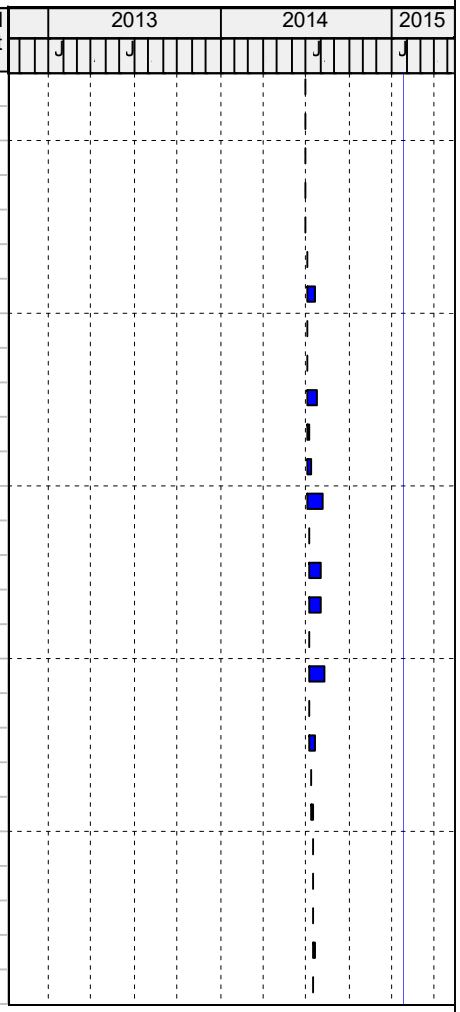



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 21-Jul-14 A | 18-Aug-14 A | |
| L15-6013 | Fire Sprinkler Branch Lines | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| L03-6000 | Tape/Finish GWB | 6 | 0 | 23-Jul-14 A | 29-Jul-14 A | |
| L11-6018 | HVAC RI | 3 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L15-6221 | Frame Unit Ceilings | 2 | 0 | 23-Jul-14 A | 01-Aug-14 A | |
| L16-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L17-6020 | Install Hollow Metal Frames | 3 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| L11-6221 | Frame Unit Ceilings | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L12-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L14-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L14-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L16-6014 | Set Tubs & Plumbing RI | 5 | 0 | 28-Jul-14 A | 18-Aug-14 A | |
| L07-6024 | Inspections for GWB Cover | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L12-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L05-6000 | Tape/Finish GWB | 6 | 0 | 31-Jul-14 A | 05-Aug-14 A | |
| L08-6024 | Inspections for GWB Cover | 2 | 0 | 31-Jul-14 A | 31-Jul-14 A | |
| L12-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L14-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L06-6000 | Tape/Finish GWB | 4 | 0 | 06-Aug-14 A | 11-Aug-14 A | |
| L09-6024 | Inspections for GWB Cover | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L07-6000 | Tape/Finish GWB | 5 | 0 | 07-Aug-14 A | 16-Aug-14 A | |
| L11-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 08-Aug-14 A | 14-Aug-14 A | |

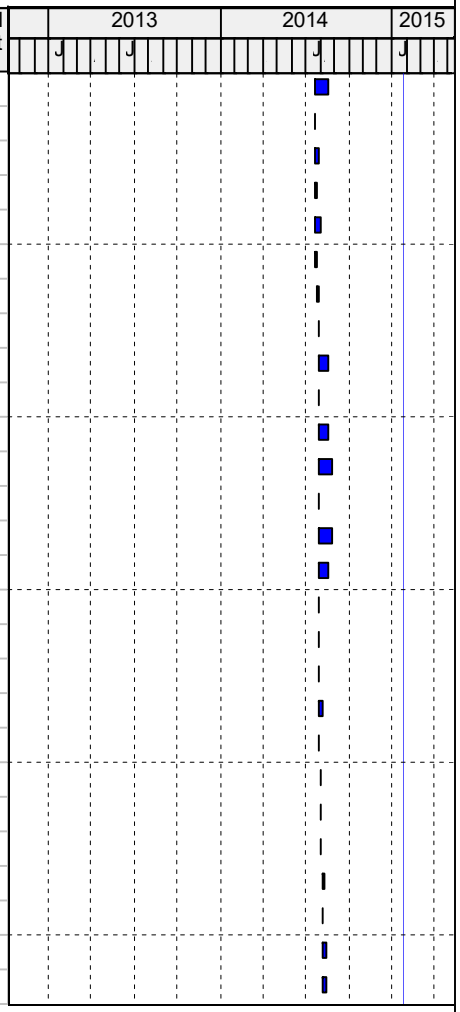


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 08-Aug-14 A | 16-Sep-14 A | |
| L10-6024 | Inspections for GWB Cover | 2 | 0 | 11-Aug-14 A | 12-Aug-14 A | |
| L09-6000 | Tape/Finish GWB | 5 | 0 | 14-Aug-14 A | 19-Aug-14 A | |
| L08-6000 | Tape/Finish GWB | 5 | 0 | 16-Aug-14 A | 21-Aug-14 A | |
| L11-6024 | Inspections for GWB Cover | 2 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L16-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 18-Aug-14 A | 29-Aug-14 A | |
| L10-6000 | Tape/Finish GWB | 5 | 0 | 19-Aug-14 A | 23-Aug-14 A | |
| L16-6221 | Frame Unit Ceilings | 4 | 0 | 21-Aug-14 A | 26-Aug-14 A | |
| L17-6018 | HVAC Rl | 3 | 0 | 21-Aug-14 A | 10-Sep-14 A | |
| L12-6024 | Inspections for GWB Cover | 2 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L15-6016 | Electrical Rl | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L15-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L11-6000 | Tape/Finish GWB | 5 | 0 | 23-Aug-14 A | 29-Aug-14 A | |
| L17-6221 | Frame Unit Ceilings | 4 | 0 | 26-Aug-14 A | 28-Aug-14 A | |
| L14-6024 | Inspections for GWB Cover | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L16-6016 | Electrical Rl | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L16-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L12-6000 | Tape/Finish GWB | 5 | 0 | 02-Sep-14 A | 08-Sep-14 A | |
| L15-6024 | Inspections for GWB Cover | 2 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L14-6000 | Tape/Finish GWB | 5 | 0 | 06-Sep-14 A | 11-Sep-14 A | |
| L15-6000 | Tape/Finish GWB | 4 | 0 | 12-Sep-14 A | 20-Sep-14 A | |
| L17-6016 | Electrical Rl | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-6028 | PreRock at Heat Pumps | 2 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L17-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |

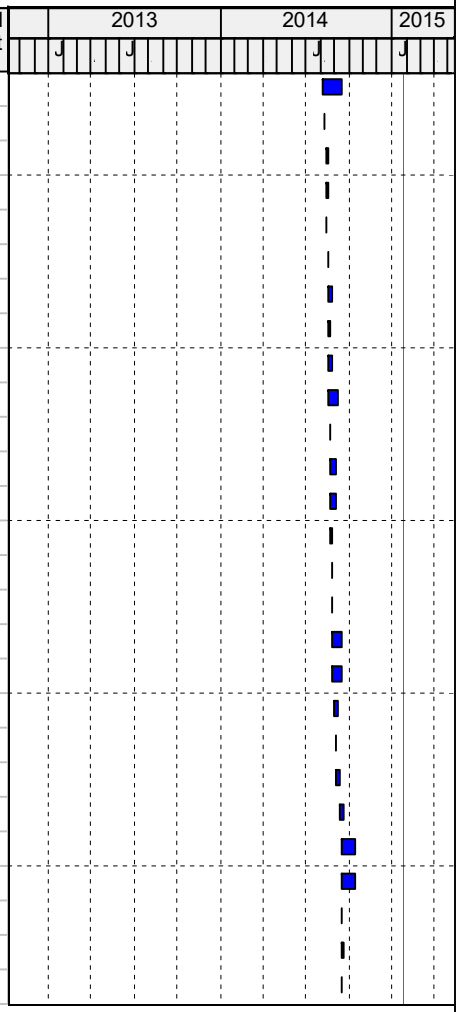


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L17-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 24-Sep-14 A | 27-Sep-14 A | |
| L17-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L16-6024 | Inspections for GWB Cover | 1 | 0 | 08-Oct-14 A | 09-Oct-14 A | |
| L16-6000 | Tape/Finish GWB | 4 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6024 | Inspections for GWB Cover | 1 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6000 | Tape/Finish GWB | 6 | 0 | 30-Oct-14 A | 07-Nov-14 A | |
| **Mechanical Penthouse** | | | | | | |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 0 | 11-Jun-14 A | 20-Jun-14 A | |
| PH-6006 | PH - Exterior Wall Framing (including PH roof parapet | 6 | 0 | 12-Jun-14 A | 14-Jul-14 A | |
| PH-6014 | PH - Plumbing/Piping RI | 40 | 0 | 25-Jun-14 A | 05-Nov-14 A | |
| PH-6002 | PH - Layout | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| PH-6008 | PH - Interior Wall Framing | 3 | 0 | 24-Jul-14 A | 08-Aug-14 A | |
| PH-6020 | PH - H Mtl Frames | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| PH-6012 | PH - Fire Sprinkler RI | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |
| PH-6018 | PH - HVAC RI | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |
| PH-6016 | PH - Electrical RI | 10 | 0 | 23-Sep-14 A | 14-Nov-14 A | |
| PH-6022 | PH - Fire Alarm / Elec Specialties RI | 10 | 0 | 23-Sep-14 A | 14-Nov-14 A | |
| **Finishes** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL4-8100 | LL4 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| LL4-8102 | LL4 - GWB Hang (incl. screw inspection) | 3 | 0 | 27-Oct-14 A | 10-Dec-14 A | |
| LL4-8114 | LL4 - Striping / Signage (DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |

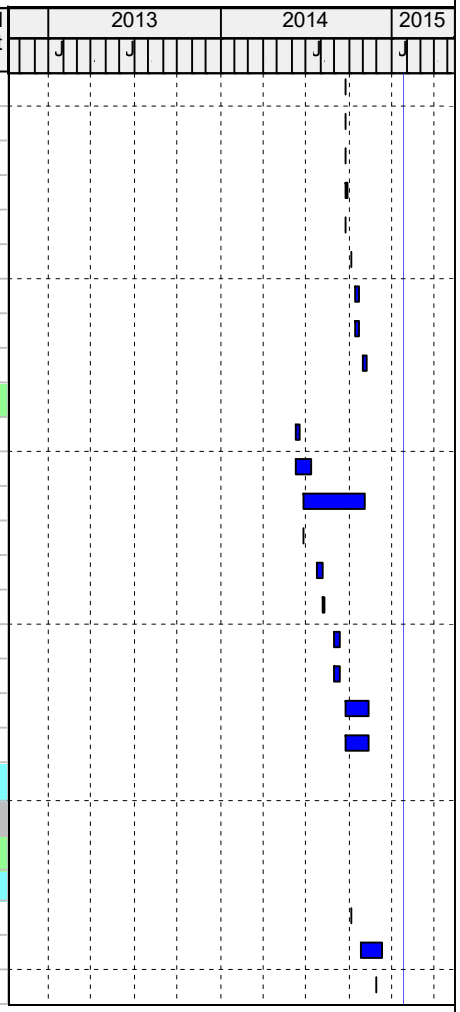



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8104 | LL4 - Int Painting | 3 | 0 | 22-Dec-14 A | 24-Dec-14 A | |
| LL4-8122 | LL4 - Plumbing Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL4-8108 | Electrical trim & finish | 5 | 2 | 29-Dec-14 A | 27-Jan-15 | 40 |
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL4-8126 | Install doors & hardware | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL4-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 1 | 22-Jan-15 A | 26-Jan-15 | 41 |
| LL4-8110 | HVAC trim | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 40 |
| LL4-8124 | Flooring - VCT | 4 | 4 | 26-Jan-15 | 29-Jan-15 | 18 |
| LL4-8134 | Clean | 2 | 2 | 18-Feb-15 | 19-Feb-15 | 35 |
| LL4-8132 | Punch | 4 | 4 | 20-Feb-15 | 25-Feb-15 | 35 |
| LL4-8214 | Floor Complete | 0 | 0 | | 25-Feb-15 | 35 |
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL3-8100 | LL3 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| LL3-8102 | LL3 - GWB Hang (incl. screw inspection) | 3 | 0 | 27-Oct-14 A | 10-Dec-14 A | |
| LL3-8114 | LL3 - Striping / Signage [DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL3-8104 | LL3 - Int Painting | 3 | 0 | 22-Dec-14 A | 24-Dec-14 A | |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL3-8108 | Electricasl trim & finish | 5 | 2 | 29-Dec-14 A | 27-Jan-15 | 40 |
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL3-8126 | Install doors & hardware | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL3-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 1 | 22-Jan-15 A | 26-Jan-15 | 41 |
| LL3-8110 | HVAC trim | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 40 |
| LL3-8124 | Flooring - VCT | 4 | 4 | 29-Jan-15 | 03-Feb-15 | 18 |
| LL3-8134 | Clean | 2 | 2 | 18-Feb-15 | 19-Feb-15 | 35 |
| LL3-8132 | Punch | 4 | 4 | 20-Feb-15 | 25-Feb-15 | 35 |
| LL3-8214 | Floor Complete | 0 | 0 | | 25-Feb-15 | 35 |

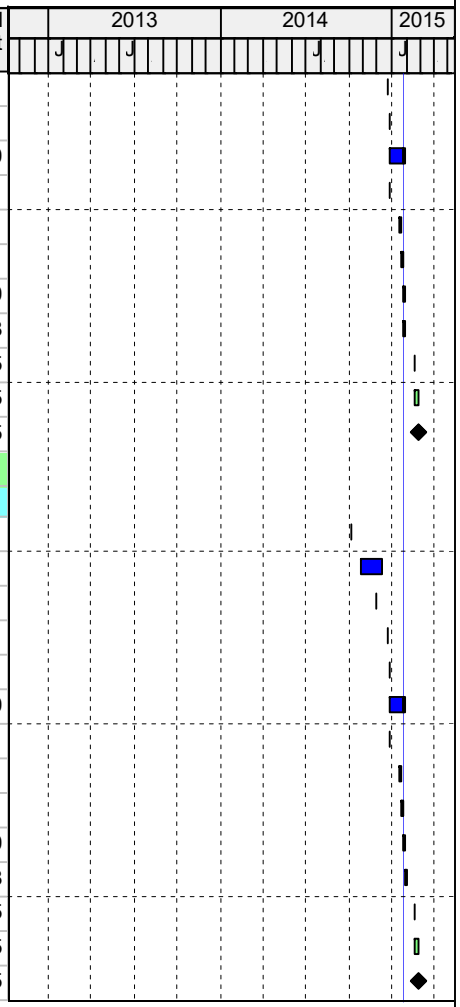



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL2E-8102 | LL2 - GWB Hang / Tape / Finish @ Electrical Rooms | 8 | 0 | 24-Jun-14 A | 03-Jul-14 A | |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish & Inspection | 6 | 0 | 16-Sep-14 A | 22-Dec-14 A | |
| LL2-8100 | LL2 - Insulation | 5 | 0 | 16-Sep-14 A | 09-Oct-14 A | |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 5 | 0 | 17-Sep-14 A | 27-Oct-14 A | |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| LL2-8104 | LL2 - Int Painting | 5 | 0 | 25-Nov-14 A | 23-Dec-14 A | |
| LL2-8114 | LL2 - Striping / Signage [DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL2-8116 | LL2 - Finish Carpentry / Millwork [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL2-8126 | Install doors & hardware | 3 | 3 | 30-Jan-15 | 03-Feb-15 | 18 |
| LL2-8124 | Flooring - VCT | 4 | 4 | 04-Feb-15 | 09-Feb-15 | 18 |
| LL2-8128 | Entry Gates at Garage | 5 | 5 | 02-Mar-15 | 06-Mar-15 | 21 |
| LL2-8136 | Chainlink Fencing / Gate @ Recycling at Garage | 5 | 5 | 02-Mar-15 | 06-Mar-15 | 21 |
| LL2-8120 | Install bollards at Garage | 5 | 5 | 02-Mar-15 | 06-Mar-15 | 21 |
| LL2-8122 | Complete MEP trim | 3 | 3 | 09-Mar-15 | 11-Mar-15 | 18 |
| LL2-8134 | Clean | 2 | 2 | 12-Mar-15 | 13-Mar-15 | 18 |
| LL2-8132 | Punch | 5 | 5 | 16-Mar-15 | 20-Mar-15 | 18 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 31-Jul-14 A | |
| LL1-Z2U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 09-May-14 A | |
| LL1-Z3U-8102 | Above Ceiling GWB (At All Areas North of Q-Line) | 5 | 0 | 10-Feb-14 A | 20-Jun-14 A | |
| L1BU-8102 | Above Ceiling GWB [including East Service Corridor] | 5 | 0 | 06-Jun-14 A | 11-Jun-14 A | |
| L1LU-8102 | Above Ceiling GWB | 5 | 0 | 24-Jun-14 A | 13-Oct-14 A | |
| L1KU-8102 | Above Ceiling GWB | 2 | 0 | 26-Jun-14 A | 22-Aug-14 A | |
| LL1-8100 | Insulation | 5 | 0 | 25-Jul-14 A | 29-Jul-14 A | |

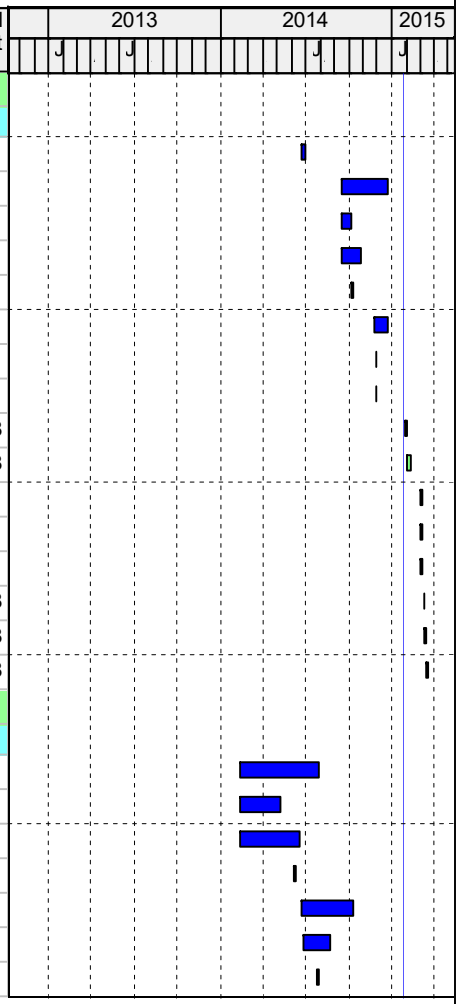


Actual Work | Remaining Work | Critical Remai... | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 28-Jul-14 A | 06-Aug-14 A | |
| LL1-Z2-8102 | GWB Hang (Walls) & Inspection | 4 | 0 | 11-Aug-14 A | 14-Aug-14 A | |
| LL1-Z2-8100 | Insulation | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| LL1-8215 | GWB Tape (Walls) | 10 | 0 | 16-Aug-14 A | 07-Nov-14 A | |
| LL1-Z3-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 15-Sep-14 A | 07-Oct-14 A | |
| LL1-Z3-8100 | Insulation | 5 | 0 | 15-Sep-14 A | 24-Sep-14 A | |
| LL1-Z2-8215 | GWB Tape (Walls/Ceilings) | 7 | 0 | 29-Sep-14 A | 07-Nov-14 A | |
| L1B-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L1K-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| LL1-Z3-8215 | GWB Tape (Walls & Ceilings) | 7 | 0 | 07-Oct-14 A | 18-Nov-14 A | |
| L1K-8102 | GWB Hang (Walls) & Inspection | 8 | 0 | 09-Oct-14 A | 31-Oct-14 A | |
| L1L-8100 | Insulation | 4 | 0 | 13-Oct-14 A | 16-Oct-14 A | |
| L1B-8102 | GWB Hang (Walls) & Inspection - Main Ballroom N/S/ | 4 | 0 | 16-Oct-14 A | 22-Oct-14 A | |
| L1L-8102 | GWB hang walls | 4 | 2 | 30-Oct-14 A | 27-Jan-15 | 0 |
| L1K-8215 | GWB Tape (Walls & Ceilings) | 4 | 0 | 05-Nov-14 A | 18-Nov-14 A | |
| LL1-Z3-8104 | Prime Paint | 4 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| LL1-8104 | Prime Paint & First Coat Finish Paint | 5 | 0 | 02-Dec-14 A | 12-Dec-14 A | |
| L1K-8106 | Wall coverings - FRP | 8 | 0 | 19-Dec-14 A | 08-Jan-15 A | |
| LL1-Z3-8114 | Ceiling grid & inspection | 4 | 0 | 13-Jan-15 A | 16-Jan-15 A | |
| LL1-8126 | Install doors & hardware | 5 | 5 | 26-Jan-15 | 30-Jan-15 | 18 |
| L1L-8215 | GWB hang ceilings | 5 | 5 | 27-Jan-15 | 02-Feb-15 | 0 |
| LL1-Z2-8104 | Paint, prime at Jr. Ballrooms | 2 | 2 | 04-Feb-15 | 05-Feb-15 | 13 |
| L1K-8114 | Ceiling grid & inspection | 5 | 5 | 04-Feb-15 | 10-Feb-15 | 9 |
| LL1-8114 | Ceiling grid & inspection | 4 | 4 | 05-Feb-15 | 10-Feb-15 | 18 |
| LL1-8116 | Finish carpentry/millwork | 10 | 10 | 06-Feb-15 | 19-Feb-15 | 18 |
| LL1-Z2-8116 | Finish carpentry/millwork | 10 | 10 | 06-Feb-15 | 19-Feb-15 | 13 |
| LL1-Z2-8106 | Wall coverings - vinyl at Jr. Ballrooms | 2 | 2 | 09-Feb-15 | 10-Feb-15 | 13 |

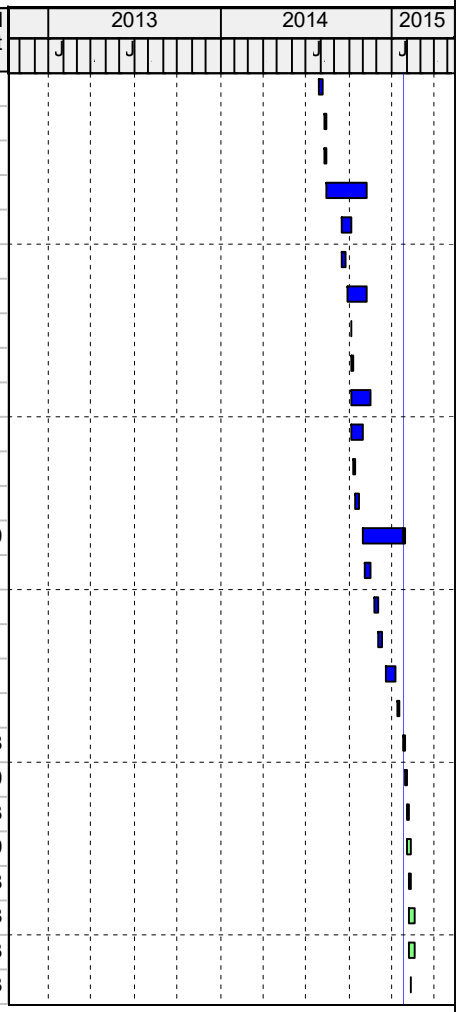


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8126 | Install doors & hardware | 5 | 5 | 09-Feb-15 | 13-Feb-15 | 21 |
| LL1-8124 | Flooring - VCT at storage areas, janitorial, mechanica | 5 | 5 | 10-Feb-15 | 16-Feb-15 | 18 |
| LL1-Z2-8114 | Ceiling grid & inspection | 5 | 5 | 10-Feb-15 | 16-Feb-15 | 22 |
| LL1-Z2-8126 | Install doors & hardware | 3 | 3 | 11-Feb-15 | 13-Feb-15 | 24 |
| LL1-Z3-8118 | Lighting & electrical drops at ceiling | 3 | 3 | 11-Feb-15 | 13-Feb-15 | 19 |
| L1B-8114 | Ceiling grid & inspection | 4 | 4 | 12-Feb-15 | 17-Feb-15 | 13 |
| L1L-8104 | Paint, prime | 2 | 2 | 12-Feb-15 | 13-Feb-15 | 0 |
| L1L-8126 | Install doors & hardware | 4 | 4 | 12-Feb-15 | 17-Feb-15 | 14 |
| LL1-8118 | Lighting & electrical drops to grid | 3 | 3 | 13-Feb-15 | 17-Feb-15 | 18 |
| LL1-Z3-8112 | Fire sprinkler drops/trim at ceiling | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 19 |
| L1K-8104 | Paint, prime | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 8 |
| LL1-8112 | Fire sprinkler drops to grid | 2 | 2 | 18-Feb-15 | 19-Feb-15 | 18 |
| LL1-Z3-8124 | Flooring - epoxy at Food Prep | 7 | 7 | 18-Feb-15 | 26-Feb-15 | 19 |
| L1L-8106 | Wall coverings - vinyl | 5 | 5 | 18-Feb-15 | 24-Feb-15 | 0 |
| L1L-8114 | Install 9-wood ceiling supports - north of Grid K | 3 | 3 | 18-Feb-15 | 20-Feb-15 | 0 |
| LL1-Z2-8118 | Lighting & electrical drops to grid | 3 | 3 | 19-Feb-15 | 23-Feb-15 | 22 |
| L1K-8124 | Flooring - VCT | 3 | 3 | 19-Feb-15 | 23-Feb-15 | 16 |
| LL1-Z2-8112 | Fire sprinkler drops to grid | 2 | 2 | 24-Feb-15 | 25-Feb-15 | 23 |
| L1K-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 24-Feb-15 | 25-Feb-15 | 8 |
| L1L-8140 | Install 9-wood ceiling - north of Grid K | 5 | 5 | 25-Feb-15 | 03-Mar-15 | 0 |
| L1K-8112 | Fire sprinkler trim | 1 | 1 | 26-Feb-15 | 26-Feb-15 | 9 |
| LL1-Z3-8116 | Finish carpentry/millwork | 3 | 3 | 27-Feb-15 | 03-Mar-15 | 21 |
| L1B-8104 | Paint, prime & first coat finish at West Ballrooms | 3 | 3 | 04-Mar-15 | 06-Mar-15 | 3 |
| L1L-8112 | Fire sprinkler trim - north of Grid K | 1 | 1 | 09-Mar-15 | 09-Mar-15 | 8 |
| L1L-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 1 | 09-Mar-15 | 09-Mar-15 | 8 |
| L1L-8124 | Flooring - wood - north of Grid K | 5 | 5 | 10-Mar-15 | 16-Mar-15 | 8 |
| LL1-Z2-8124 | Flooring - VCT at service corridor | 2 | 2 | 11-Mar-15 | 12-Mar-15 | 14 |

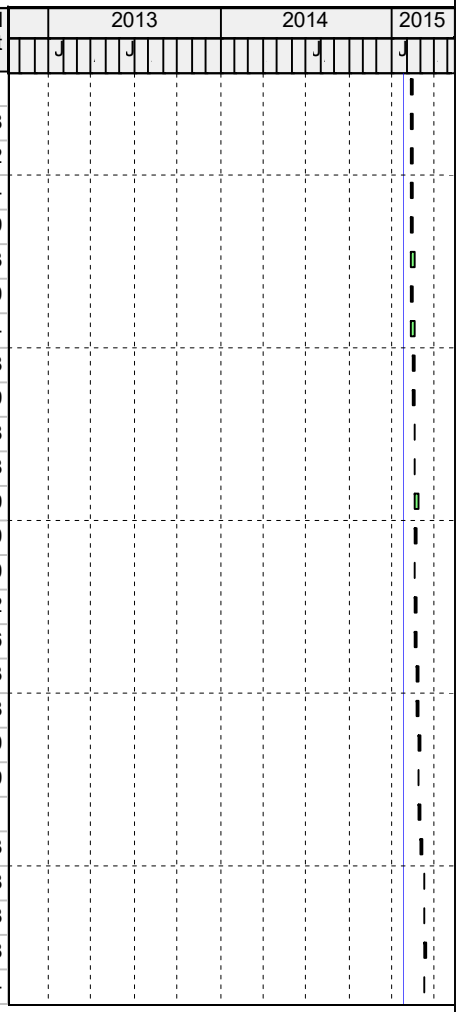



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8140 | Acoustical ceiling tile | 3 | 3 | 11-Mar-15 | 13-Mar-15 | 16 |
| L1K-8116 | Finish carpentry/millwork | 2 | 2 | 11-Mar-15 | 12-Mar-15 | 15 |
| L1K-8126 | Install doors & hardware | 3 | 3 | 11-Mar-15 | 13-Mar-15 | 14 |
| LL1-8140 | Acoustical ceiling tile | 3 | 3 | 13-Mar-15 | 17-Mar-15 | 13 |
| LL1-Z2-8140 | Acoustical ceiling tile | 2 | 2 | 13-Mar-15 | 16-Mar-15 | 14 |
| LL1-Z3-8134 | Clean | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 16 |
| L1B-8126 | Install doors & hardware at Ballrooms | 5 | 5 | 16-Mar-15 | 20-Mar-15 | 4 |
| LL1-Z2-8134 | Clean | 3 | 3 | 17-Mar-15 | 19-Mar-15 | 14 |
| L1L-8116 | Finish carpentry/millwork - north of Grid K | 10 | 10 | 17-Mar-15 | 30-Mar-15 | 8 |
| LL1-8134 | Clean | 3 | 3 | 18-Mar-15 | 20-Mar-15 | 13 |
| LL1-Z3-8132 | Punch | 5 | 5 | 18-Mar-15 | 24-Mar-15 | 16 |
| L1K-8140 | Acoustical ceiling tile | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 12 |
| LL1-Z2-8132 | Punch | 5 | 5 | 20-Mar-15 | 26-Mar-15 | 14 |
| LL1-8132 | Punch | 5 | 5 | 23-Mar-15 | 27-Mar-15 | 13 |
| L1B-8116 | Finish carpentry/millwork at Ballrooms | 10 | 10 | 25-Mar-15 | 07-Apr-15 | 2 |
| L1K-8134 | Clean | 2 | 2 | 26-Mar-15 | 27-Mar-15 | 8 |
| L1K-8132 | Punch | 5 | 5 | 30-Mar-15 | 03-Apr-15 | 8 |
| L1B-8124 | Flooring - carpet at Ballrooms | 5 | 5 | 03-Apr-15 | 09-Apr-15 | 0 |
| L1B-8140 | Acoustical ceiling tile | 2 | 2 | 10-Apr-15 | 13-Apr-15 | 0 |
| L1B-8134 | Clean | 2 | 2 | 14-Apr-15 | 15-Apr-15 | 0 |
| L1L-8134 | Clean | 2 | 2 | 14-Apr-15 | 15-Apr-15 | 0 |
| L1B-8132 | Punch | 5 | 5 | 16-Apr-15 | 22-Apr-15 | 5 |
| L1L-8132 | Punch | 5 | 5 | 16-Apr-15 | 22-Apr-15 | 5 |
| **Corridors / Common / Public Areas** | | | | | | |
| LL1-8200 | Wall coverings - vinyl | 4 | 0 | 17-Dec-14 A | 19-Jan-15 A | |
| LL1-Z3-8200 | Paint, first coat finish | 4 | 0 | 07-Jan-15 A | 12-Jan-15 A | |
| LL1-Z3-8204 | HVAC drops/trim at ceiling | 2 | 2 | 27-Jan-15 | 28-Jan-15 | 28 |

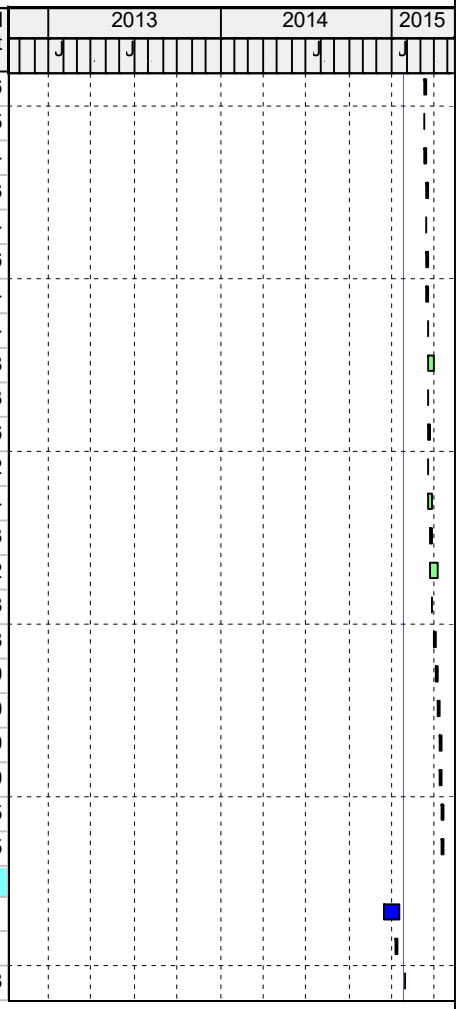


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-8200 | Paint, first coat finish at Jr. Ballrooms | 1 | 1 | 06-Feb-15 | 06-Feb-15 | 13 |
| LL1-8204 | HVAC drops/trim to grid | 2 | 2 | 11-Feb-15 | 12-Feb-15 | 18 |
| L1L-8200 | Paint, first coat finish | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 0 |
| LL1-Z2-8204 | HVAC drops/trim to grid | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 22 |
| L1K-8200 | Paint, first coat finish | 1 | 1 | 19-Feb-15 | 19-Feb-15 | 8 |
| LL1-8201 | Paint, final coat & touch-up | 2 | 2 | 20-Feb-15 | 23-Feb-15 | 29 |
| L1K-8204 | HVAC drops/trim at celing | 2 | 2 | 20-Feb-15 | 23-Feb-15 | 8 |
| LL1-Z2-8201 | Paint, final coat & touch-up | 2 | 2 | 27-Feb-15 | 02-Mar-15 | 24 |
| L1L-8204 | HVAC trim at ceiling - north of Grid K | 1 | 1 | 04-Mar-15 | 04-Mar-15 | 8 |
| LL1-Z3-8201 | Paint, final coat & touch-up | 3 | 3 | 11-Mar-15 | 13-Mar-15 | 16 |
| L1B-8200 | Paint, prime & first coat finish at East Ballroom | 3 | 3 | 11-Mar-15 | 13-Mar-15 | 0 |
| L1K-8201 | Paint, final coat & touch-up | 2 | 2 | 24-Mar-15 | 25-Mar-15 | 8 |
| LL1-Z3-8214 | LL1, Zone 3 Complete | 0 | 0 | | 24-Mar-15 | 16 |
| LL1-Z2-8214 | LL1 Zone 2 Complete | 0 | 0 | | 26-Mar-15 | 14 |
| LL1-8214 | LL1, Zone 1 Complete | 0 | 0 | | 27-Mar-15 | 13 |
| L1K-8214 | L1, Zone 1 Complete | 0 | 0 | | 03-Apr-15 | 8 |
| L1B-8201 | Paint, final coat & touch-up | 2 | 2 | 10-Apr-15 | 13-Apr-15 | 0 |
| L1L-8201 | Paint, final coat & touch-up | 2 | 2 | 10-Apr-15 | 13-Apr-15 | 0 |
| L1B-8214 | L1, Zone 2 Complete | 0 | 0 | | 22-Apr-15 | 5 |
| L1L-8214 | L1, Zone 4 Complete | 0 | 0 | | 22-Apr-15 | 5 |
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8100 | L2 - Insulation - North Half | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L02-8102 | L2 - GWB Hang / Tape / Finish - North Half | 7 | 0 | 23-Oct-14 A | 17-Dec-14 A | |
| L02-8104 | Paint, prime & first coat finish at north half | 3 | 3 | 26-Jan-15 | 28-Jan-15 | 26 |
| L02-8106 | Wall coverings - vinyl at south half | 4 | 4 | 26-Jan-15 | 29-Jan-15 | 29 |
| L02-8126 | Install doors & hardware at south half | 5 | 5 | 30-Jan-15 | 05-Feb-15 | 29 |

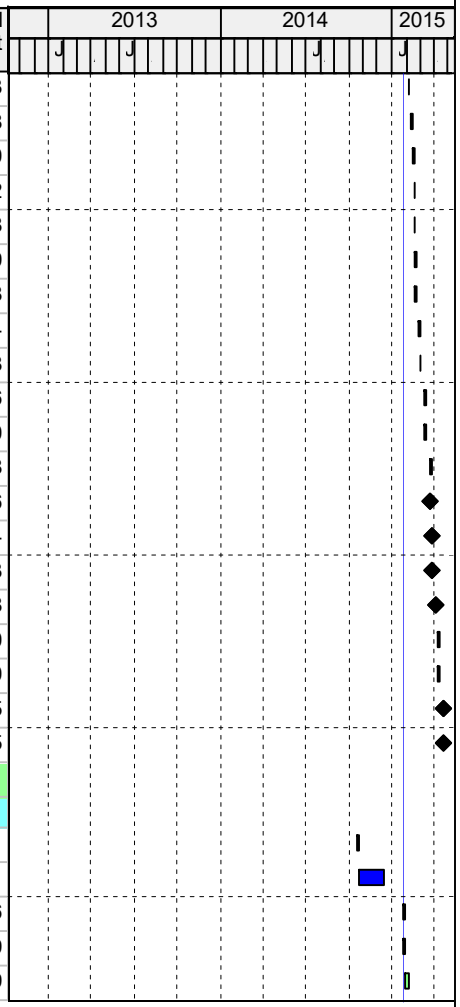


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8110 | HVAC drops/trim at south half | 2 | 2 | 09-Feb-15 | 10-Feb-15 | 21 |
| L02-8120 | Ceramic tile | 5 | 5 | 10-Feb-15 | 16-Feb-15 | 25 |
| L02-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 11-Feb-15 | 13-Feb-15 | 21 |
| L02-8112 | Fire sprinkler drops/trim at south half | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 32 |
| L02-8122 | Plumbing fixtures & trim | 5 | 5 | 17-Feb-15 | 23-Feb-15 | 25 |
| L02-8124 | Flooring - carpet | 5 | 5 | 20-Feb-15 | 26-Feb-15 | 21 |
| L02-8128 | Install bathroom accessories | 5 | 5 | 24-Feb-15 | 02-Mar-15 | 25 |
| L02-8136 | Lockers / Benches @ Locker Rooms | 5 | 5 | 24-Feb-15 | 02-Mar-15 | 25 |
| L02-8116 | Finish carpentry/millwork at south half | 4 | 4 | 27-Feb-15 | 04-Mar-15 | 21 |
| L02-8108 | Complete MEP trim at south half | 2 | 2 | 05-Mar-15 | 06-Mar-15 | 21 |
| L02-8134 | Clean | 2 | 2 | 09-Mar-15 | 10-Mar-15 | 21 |
| L02-8132 | Punch | 5 | 5 | 11-Mar-15 | 17-Mar-15 | 21 |
| **Corridors** | | | | | | |
| L02-8200 | Paint, final coat & touch-up at south half | 2 | 2 | 05-Mar-15 | 06-Mar-15 | 21 |
| L02-8214 | Floor Complete | 0 | 0 | | 17-Mar-15 | 21 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L03-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L04-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L05-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L06-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L07-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L08-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L09-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L10-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L11-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |

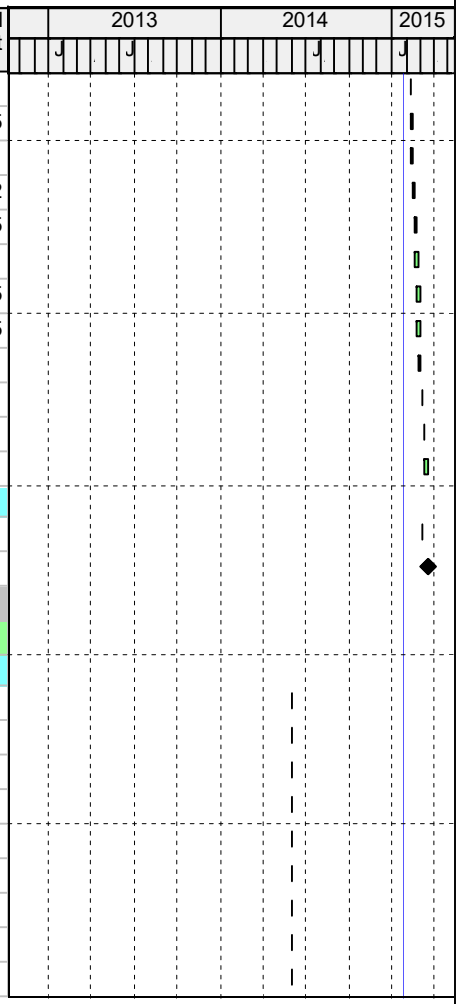



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L14-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L15-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L16-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L17-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L03-8102S | Stock GWB | 2 | 0 | 27-Jun-14 A | 08-Jul-14 A | |
| L04-8102 | Hang GWB & Inspection | 4 | 0 | 07-Jul-14 A | 16-Jul-14 A | |
| L04-8102S | Stock GWB | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-8102 | Hang GWB & Inspection | 5 | 0 | 09-Jul-14 A | 22-Jul-14 A | |
| L05-8102S | Stock GWB | 2 | 0 | 10-Jul-14 A | 14-Jul-14 A | |
| L05-8102 | Hang GWB & Inspection | 4 | 0 | 17-Jul-14 A | 23-Jul-14 A | |
| L06-8102S | Stock GWB | 2 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L04-8104 | Paint (Prime) | 2 | 0 | 28-Jul-14 A | 05-Aug-14 A | |
| L03-8104 | Paint (Prime) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L03-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L07-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L08-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L06-8102 | Hang GWB & Inspection | 5 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L07-8102 | Hang GWB & Inspection | 6 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L04-8105 | Paint (First Coat & Ceilings) | 5 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L05-8104 | Paint (Prime) | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| L09-8102S | Stock GWB | 2 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 07-Aug-14 A | 11-Aug-14 A | |
| L09-8102 | Hang GWB & Inspection | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| L08-8102 | Hang GWB & Inspection | 6 | 0 | 11-Aug-14 A | 15-Aug-14 A | |
| L06-8104 | Paint (Prime) | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L10-8102S | Stock GWB | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |

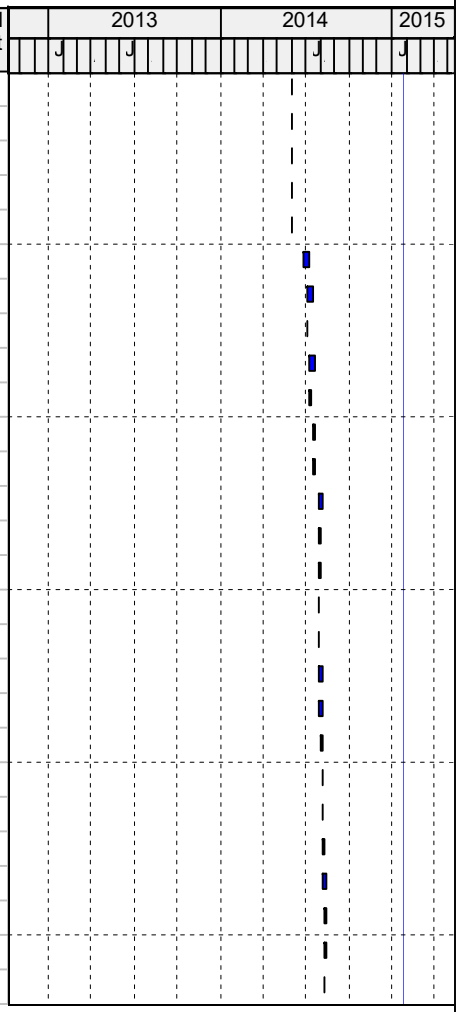



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8102 | Hang GWB & Inspection | 4 | 0 | 13-Aug-14 A | 18-Aug-14 A | |
| L06-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 14-Aug-14 A | 18-Aug-14 A | |
| L11-8102S | Stock GWB | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L07-8104 | Paint (Prime) | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L11-8102 | Hang GWB & Inspection | 4 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| L07-8105 | Paint (First Coat & Ceilings) | 4 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L09-8104 | Paint (Prime) | 2 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L08-8104 | Paint (Prime) | 2 | 0 | 22-Aug-14 A | 25-Aug-14 A | |
| L12-8102 | Hang GWB & Inspection | 4 | 0 | 22-Aug-14 A | 30-Aug-14 A | |
| L12-8102S | Stock GWB | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8108 | Elec Trim / Finish | 4 | 0 | 25-Aug-14 A | 04-Sep-14 A | |
| L08-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L03-8118 | Fire Alarm Trim / Finish | 3 | 0 | 27-Aug-14 A | 29-Sep-14 A | |
| L14-8102S | Stock GWB | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L09-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 29-Aug-14 A | 09-Sep-14 A | |
| L14-8102 | Hang GWB & Inspection | 5 | 0 | 29-Aug-14 A | 05-Sep-14 A | |
| L03-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 02-Sep-14 A | 05-Sep-14 A | |
| L04-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 04-Sep-14 A | 09-Sep-14 A | |
| L10-8104 | Paint (Prime) | 2 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| L15-8102S | Stock GWB | 1 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L15-8102 | Hang GWB & Inspection | 5 | 0 | 06-Sep-14 A | 12-Sep-14 A | |
| L03-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8108 | Elec Trim / Finish | 4 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L04-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 11-Sep-14 A | |
| L05-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 08-Sep-14 A | 12-Sep-14 A | |
| L10-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 08-Sep-14 A | 12-Sep-14 A | |
| L11-8104 | Paint (Prime) | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |

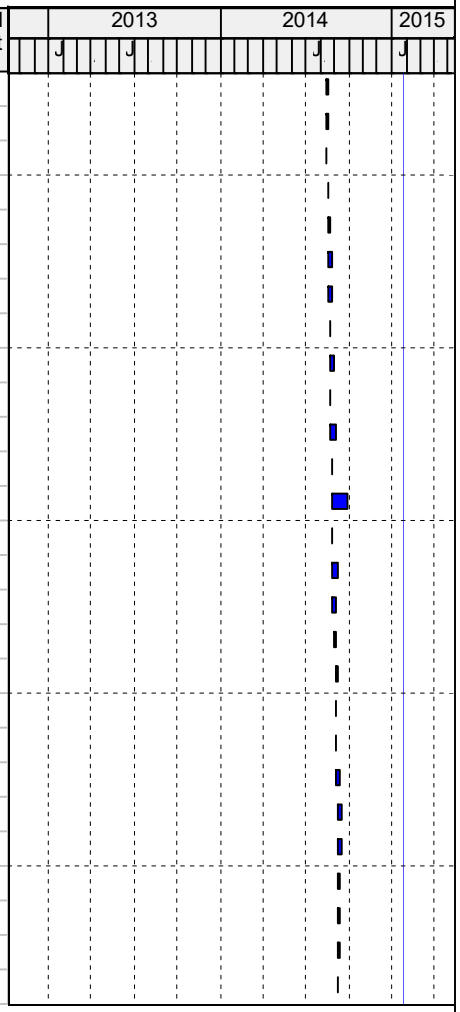



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L04-8116 | Install Base at Guestrooms | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L11-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 10-Sep-14 A | 22-Sep-14 A | |
| L03-8116 | Install Base at Guestrooms | 5 | 0 | 12-Sep-14 A | 16-Sep-14 A | |
| L12-8104 | Paint (Prime) | 2 | 0 | 12-Sep-14 A | 17-Sep-14 A | |
| L05-8116 | Install Base at Guestrooms | 5 | 0 | 16-Sep-14 A | 24-Sep-14 A | |
| L06-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L05-8108 | Elec Trim / Finish | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L07-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 17-Sep-14 A | 23-Sep-14 A | |
| L12-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 17-Sep-14 A | 06-Oct-14 A | |
| L06-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L07-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L14-8104 | Paint (Prime) | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L06-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L06-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L08-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L14-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 24-Sep-14 A | 06-Oct-14 A | |
| L15-8104 | Paint (Prime) | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L03-8110 | HVAC Grilles & Registers | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L03-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8118 | Fire Alarm Trim / Finish | 3 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L10-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L08-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 30-Sep-14 A | 06-Oct-14 A | |
| L03-8126 | Install Doors | 3 | 0 | 01-Oct-14 A | 07-Oct-14 A | |

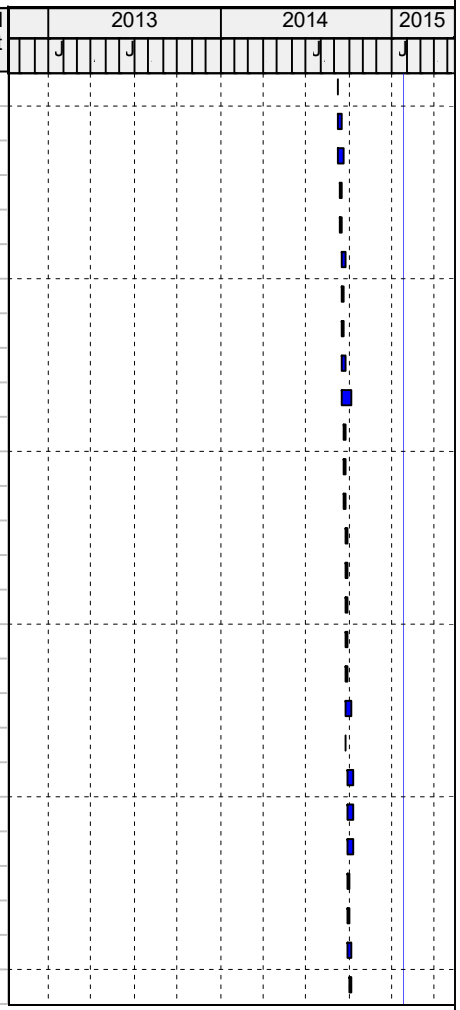



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 01-Oct-14 A | 28-Oct-14 A | |
| L04-8126 | Install Doors | 3 | 0 | 02-Oct-14 A | 09-Oct-14 A | |
| L08-8116 | Install Base at Guestrooms | 5 | 0 | 02-Oct-14 A | 08-Oct-14 A | |
| L04-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8118 | Fire Alarm Trim / Finish | 3 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8108 | Elec Trim / Finish | 4 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L15-8105 | Paint - First Coast & Ceilings | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8126 | Install Doors | 3 | 0 | 08-Oct-14 A | 10-Oct-14 A | |
| L09-8116 | Install Base and Door Thresholds | 5 | 0 | 08-Oct-14 A | 15-Oct-14 A | |
| L09-8124 | Install Flooring | 5 | 0 | 08-Oct-14 A | 14-Oct-14 A | |
| L16-8102S | Stock GWB | 1 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L09-8112 | Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 10-Oct-14 A | |
| L16-8102 | Hang GWB & Inspection | 4 | 0 | 10-Oct-14 A | 17-Oct-14 A | |
| L06-8118 | Fire Alarm Trim / Finish | 3 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L09-8108 | Lighting and Electrical Trim | 3 | 0 | 13-Oct-14 A | 15-Oct-14 A | |
| L10-8124 | Install Flooring | 5 | 0 | 13-Oct-14 A | 16-Oct-14 A | |
| L11-8112 | Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L03-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 14-Oct-14 A | 04-Nov-14 A | |
| L06-8110 | HVAC Grilles & Registers | 2 | 0 | 14-Oct-14 A | 21-Oct-14 A | |
| L06-8126 | Install Doors | 2 | 0 | 14-Oct-14 A | 20-Oct-14 A | |
| L07-8118 | Fire Alarm Trim / Finish | 3 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L12-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L14-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L08-8118 | Fire Alarm Trim / Finish | 3 | 0 | 15-Oct-14 A | 16-Oct-14 A | |
| L10-8116 | Install Base and Door Thresholds | 5 | 0 | 15-Oct-14 A | 23-Oct-14 A | |
| L15-8112 | Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 16-Oct-14 A | |

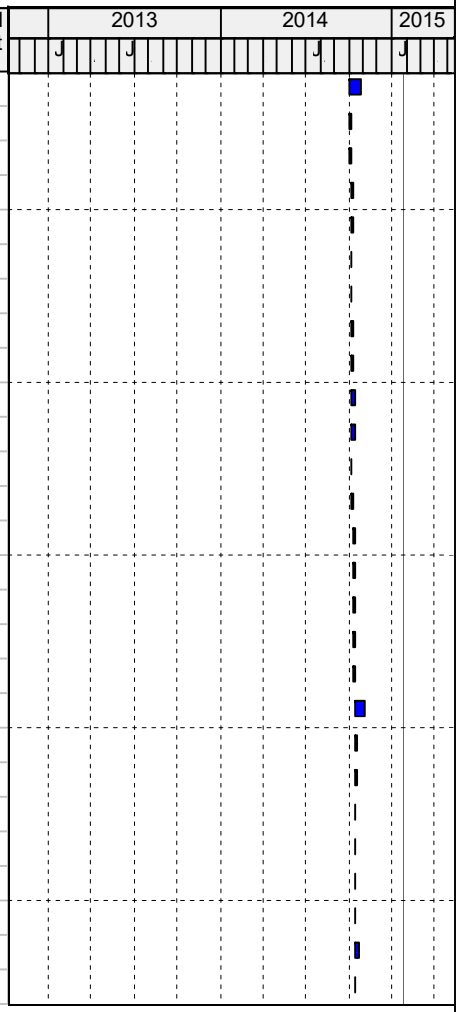



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 16-Oct-14 A | 11-Nov-14 A | |
| L11-8124 | Install Flooring | 5 | 0 | 16-Oct-14 A | 22-Oct-14 A | |
| L17-8102S | Stock GWB | 1 | 0 | 17-Oct-14 A | 17-Oct-14 A | |
| L07-8126 | Install Doors | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |
| L09-8118 | Fire Alarm Trim | 2 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| L05-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 21-Oct-14 A | 14-Nov-14 A | |
| L08-8126 | Install Doors | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L10-8118 | Fire Alarm Trim | 2 | 0 | 21-Oct-14 A | 21-Oct-14 A | |
| L09-8126 | Install Doors | 2 | 0 | 22-Oct-14 A | 23-Oct-14 A | |
| L11-8118 | Fire Alarm Trim | 2 | 0 | 22-Oct-14 A | 22-Oct-14 A | |
| L06-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 23-Oct-14 A | 19-Nov-14 A | |
| L10-8126 | Install Doors | 2 | 0 | 23-Oct-14 A | 27-Oct-14 A | |
| L12-8124 | Install Flooring | 5 | 0 | 23-Oct-14 A | 29-Oct-14 A | |
| L12-8118 | Fire Alarm Trim | 2 | 0 | 23-Oct-14 A | 23-Oct-14 A | |
| L11-8116 | Install Base and Door Thresholds | 5 | 0 | 24-Oct-14 A | 26-Nov-14 A | |
| L07-8110 | HVAC Grilles & Registers | 2 | 0 | 27-Oct-14 A | 28-Oct-14 A | |
| L10-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |
| L11-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |
| L17-8102 | Hang GWB & Inspection | 4 | 0 | 27-Oct-14 A | 03-Nov-14 A | |
| L07-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 28-Oct-14 A | 26-Nov-14 A | |
| L08-8120 | Bathrooms - Install Countertops | 3 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L11-8126 | Install Doors | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L12-8108 | Lighting and Electrical Trim | 3 | 0 | 28-Oct-14 A | 30-Oct-14 A | |
| L12-8116 | Install Base and Door Thresholds | 5 | 0 | 28-Oct-14 A | 03-Dec-14 A | |
| L14-8118 | Fire Alarm Trim | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L05-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Oct-14 A | 31-Oct-14 A | |
| L06-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Oct-14 A | 31-Oct-14 A | |

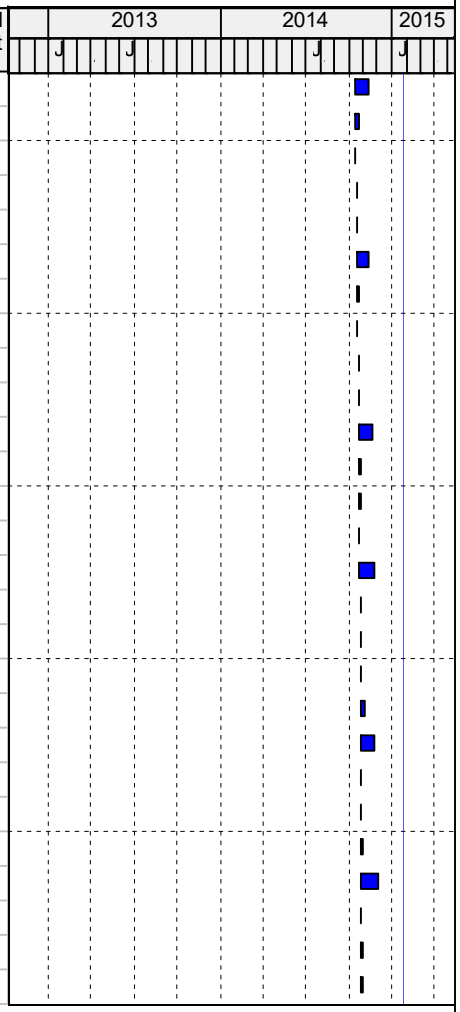



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L14-8108 | Lighting and Electrical Trim | 3 | 0 | 29-Oct-14 A | 03-Nov-14 A | |
| L14-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8118 | Fire Alarm Trim | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L04-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 30-Oct-14 A | 04-Nov-14 A | |
| L07-8120 | Bathrooms - Install Countertops | 3 | 0 | 03-Nov-14 A | 05-Nov-14 A | |
| L08-8110 | HVAC Grilles & Registers | 2 | 0 | 03-Nov-14 A | 04-Nov-14 A | |
| L09-8120 | Bathrooms - Install Countertops | 3 | 0 | 03-Nov-14 A | 05-Nov-14 A | |
| L10-8120 | Bathrooms - Install Countertops | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| L15-8108 | Lighting and Electrical Trim | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| L11-8120 | Bathrooms - Install Countertops | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| L16-8104 | Paint - Prime | 2 | 0 | 05-Nov-14 A | 06-Nov-14 A | |
| L05-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 07-Nov-14 A | 12-Nov-14 A | |
| L16-8105 | Paint - First Coat & Ceilings | 3 | 0 | 07-Nov-14 A | 11-Nov-14 A | |
| L12-8120 | Bathrooms - Install Countertops | 3 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L14-8124 | Install Flooring | 5 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L06-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 13-Nov-14 A | 17-Nov-14 A | |
| L15-8124 | Install Flooring | 5 | 0 | 17-Nov-14 A | 25-Nov-14 A | |
| L17-8104 | Paint - Prime | 2 | 0 | 17-Nov-14 A | 18-Nov-14 A | |
| L14-8116 | Install Base and Door Thresholds | 5 | 0 | 18-Nov-14 A | 08-Dec-14 A | |
| L16-8126 | Install Doors | 2 | 0 | 18-Nov-14 A | 19-Nov-14 A | |
| L07-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 19-Nov-14 A | 25-Nov-14 A | |
| L15-8116 | Install Base and Door Thresholds | 5 | 0 | 20-Nov-14 A | 08-Dec-14 A | |
| L03-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L04-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L05-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |

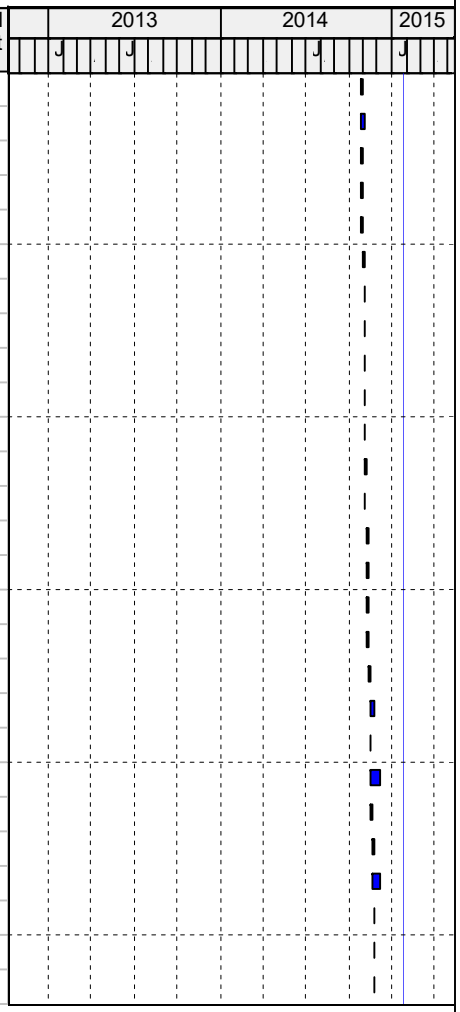



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| L17-8105 | Paint - First Coat & Ceilings | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L16-8124 | Install Flooring | 5 | 0 | 25-Nov-14 A | 03-Dec-14 A | |
| L16-8112 | Fire Sprinkler Trim | 2 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| L16-8118 | Fire Alarm Trim | 2 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| L06-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L07-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L08-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 01-Dec-14 A | 08-Dec-14 A | |
| L08-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L09-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 01-Dec-14 A | 10-Dec-14 A | |
| L16-8108 | Lighting and Electrical Trim | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L17-8126 | Install Doors | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| L16-8116 | Install Base and Door Thresholds | 5 | 0 | 02-Dec-14 A | 15-Dec-14 A | |
| L17-8112 | Fire Sprinkler Trim | 2 | 0 | 02-Dec-14 A | 02-Dec-14 A | |
| L09-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 03-Dec-14 A | 08-Dec-14 A | |
| L09-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L10-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L11-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L17-8118 | Fire Alarm Trim | 2 | 0 | 03-Dec-14 A | 03-Dec-14 A | |
| L12-8107 | Paint Final Coat | 3 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L14-8120 | Bathrooms - Install Countertops | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L17-8108 | Lighting and Electrical Trim | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L10-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L15-8120 | Bathrooms - Install Countertops | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 10-Dec-14 A | 16-Dec-14 A | |
| L11-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 10-Dec-14 A | 24-Dec-14 A | |
| L04-8132 | Punchlist @ Guestrooms | 4 | 2 | 11-Dec-14 A | 27-Jan-15 | 31 |

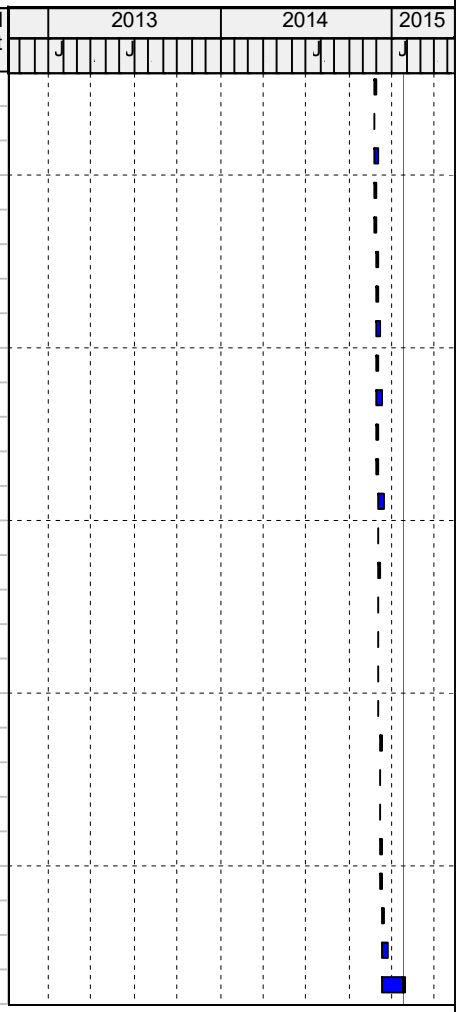



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8134 | Final Clean @ Guestrooms | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L05-8132 | Punchlist @ Guestrooms | 4 | 3 | 12-Dec-14 A | 28-Jan-15 | 30 |
| L05-8134 | Final Clean @ Guestrooms | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L11-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 12-Dec-14 A | 17-Dec-14 A | |
| L06-8134 | Final Clean @ Guestrooms | 5 | 0 | 13-Dec-14 A | 13-Dec-14 A | |
| L12-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 15-Dec-14 A | 18-Dec-14 A | |
| L17-8124 | Install Flooring | 5 | 0 | 15-Dec-14 A | 18-Dec-14 A | |
| L17-8116 | Install Base and Door Thresholds | 5 | 0 | 18-Dec-14 A | 30-Dec-14 A | |
| L12-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| L14-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| L15-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 29-Dec-14 A | 05-Jan-15 A | |
| L16-8120 | Bathrooms - Install countertops | 3 | 0 | 29-Dec-14 A | 09-Jan-15 A | |
| L14-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 30-Dec-14 A | 05-Jan-15 A | |
| L15-8122 | Bathrooms - Plumbing fixtures & trim | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L16-8128 | Bathrooms - Install shower/tub surrounds | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L16-8122 | Bathrooms - Plumbing fixtures & trim | 3 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8128 | Bathrooms - Install shower/tub surrounds | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L09-8110 | HVAC grilles & registers | 2 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| L11-8110 | HVAC grilles & registers | 2 | 1 | 21-Jan-15 A | 27-Jan-15 | 27 |
| L12-8110 | HVAC grilles & registers | 2 | 1 | 21-Jan-15 A | 27-Jan-15 | 27 |
| L14-8110 | HVAC grilles & registers | 2 | 1 | 21-Jan-15 A | 27-Jan-15 | 27 |
| L03-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 30 |
| L04-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 32 |
| L05-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 32 |
| L06-8132 | Punchlist @ Guestrooms | 4 | 4 | 26-Jan-15 | 29-Jan-15 | 29 |
| L07-8132 | Punchlist @ Guestrooms | 4 | 4 | 26-Jan-15 | 29-Jan-15 | 29 |
| L07-8134 | Final clean at Guestrooms | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 31 |

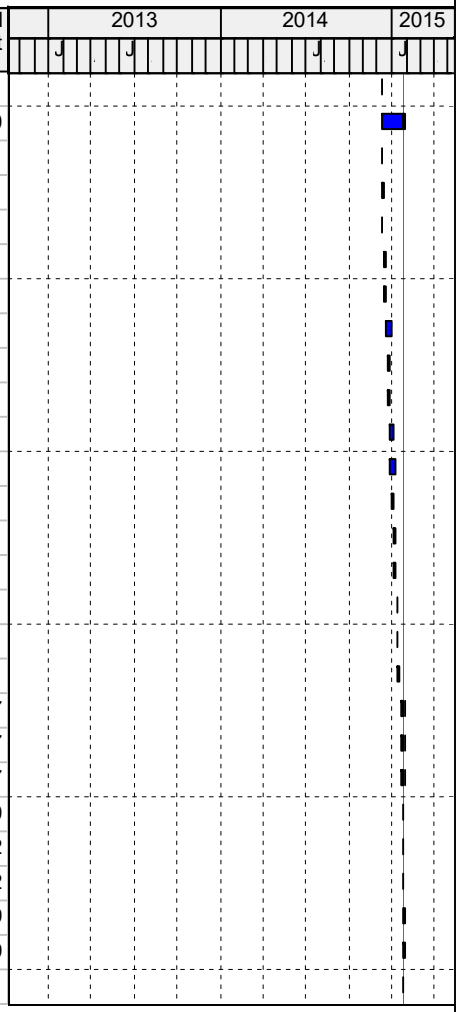


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8132 | Punchlist @ Guestrooms | 3 | 3 | 26-Jan-15 | 28-Jan-15 | 30 |
| L08-8134 | Final clean at Guestrooms | 1 | 1 | 26-Jan-15 | 26-Jan-15 | 31 |
| L09-8132 | Punchlist @ Guestrooms | 3 | 3 | 26-Jan-15 | 28-Jan-15 | 30 |
| L10-8110 | HVAC grilles & registers | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 25 |
| L17-8120 | Bathrooms - Install countertops | 3 | 3 | 26-Jan-15 | 28-Jan-15 | 28 |
| L09-8134 | Final clean at Guestrooms | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 31 |
| L11-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 30 |
| L12-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 31 |
| L14-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 32 |
| L15-8110 | HVAC grilles & registers | 2 | 2 | 27-Jan-15 | 28-Jan-15 | 27 |
| L15-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 32 |
| L16-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 33 |
| L06-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 30 |
| L07-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 30 |
| L10-8132 | Punchlist @ Guestrooms | 3 | 3 | 28-Jan-15 | 30-Jan-15 | 28 |
| L10-8134 | Final clean at Guestrooms | 1 | 1 | 28-Jan-15 | 28-Jan-15 | 30 |
| L11-8132 | Punchlist @ Guestrooms | 4 | 4 | 28-Jan-15* | 02-Feb-15 | 31 |
| L12-8132 | Punchlist @ Guestrooms | 4 | 4 | 28-Jan-15 | 02-Feb-15 | 31 |
| L14-8107 | Paint, final coat & touch-up | 3 | 3 | 28-Jan-15 | 30-Jan-15 | 29 |
| L16-8110 | HVAC grilles & registers | 2 | 2 | 28-Jan-15 | 29-Jan-15 | 27 |
| L15-8107 | Paint, final coat & touch-up | 3 | 3 | 29-Jan-15 | 02-Feb-15 | 28 |
| L17-8122 | Bathrooms - Plumbing fixtures & trim | 3 | 3 | 29-Jan-15 | 02-Feb-15 | 28 |
| L17-8110 | HVAC grilles & registers | 2 | 2 | 29-Jan-15 | 30-Jan-15 | 27 |
| L03-8132 | Punchlist @ Guestrooms | 4 | 4 | 30-Jan-15 | 04-Feb-15 | 30 |
| L03-8134 | Final clean at Guestrooms | 1 | 1 | 30-Jan-15* | 30-Jan-15 | 27 |
| L08-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 28 |
| L16-8107 | Paint, final coat & touch-up | 3 | 3 | 30-Jan-15 | 03-Feb-15 | 28 |

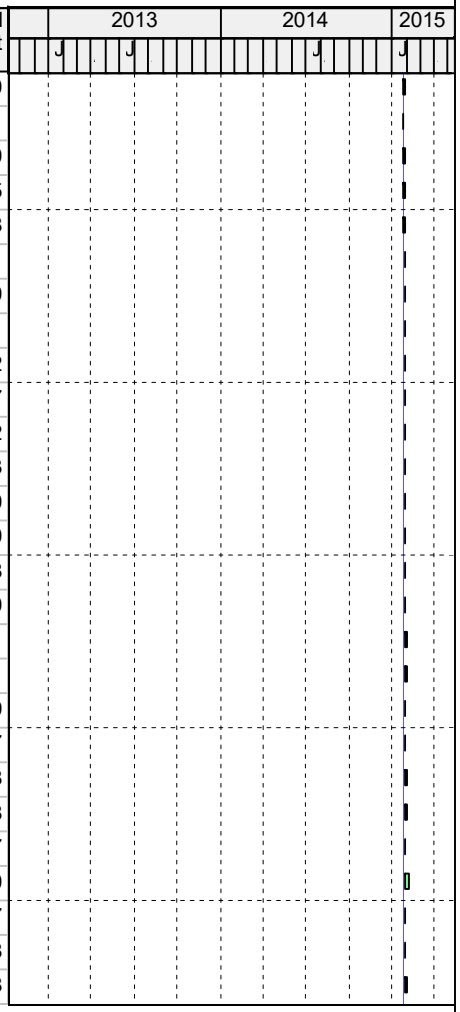



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 30 |
| L11-8134 | Final clean at Guestrooms | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 27 |
| L14-8132 | Punchlist @ Guestrooms | 4 | 4 | 02-Feb-15 | 05-Feb-15 | 29 |
| L17-8107 | Paint, final coat & touch-up | 3 | 3 | 02-Feb-15 | 04-Feb-15 | 27 |
| L09-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 26 |
| L10-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 26 |
| L12-8134 | Final clean at Guestrooms | 1 | 1 | 03-Feb-15 | 03-Feb-15 | 27 |
| L15-8132 | Punchlist @ Guestrooms | 4 | 4 | 03-Feb-15 | 06-Feb-15 | 28 |
| L14-8134 | Final clean at Guestrooms | 1 | 1 | 04-Feb-15 | 04-Feb-15 | 27 |
| L16-8132 | Punchlist @ Guestrooms | 3 | 3 | 04-Feb-15 | 06-Feb-15 | 28 |
| L15-8134 | Final clean at Guestrooms | 1 | 1 | 05-Feb-15 | 05-Feb-15 | 27 |
| L17-8132 | Punchlist @ Guestrooms | 3 | 3 | 05-Feb-15 | 09-Feb-15 | 27 |
| L16-8134 | Final clean at Guestrooms | 1 | 1 | 06-Feb-15 | 06-Feb-15 | 27 |
| L17-8134 | Final clean at Guestrooms | 1 | 1 | 09-Feb-15 | 09-Feb-15 | 27 |
| **Pool Area** | | | | | | |
| L03-8216 | Install pool tile, coping and depth markers | 5 | 5 | 12-Mar-15 | 18-Mar-15 | 2 |
| **Corridors / Common / Public Areas** | | | | | | |
| L03-8200 | Vinyl Wall Coverings | 3 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L04-8200 | Vinyl Wall Coverings | 5 | 0 | 06-Aug-14 A | 12-Aug-14 A | |
| L05-8200 | Vinyl Wall Coverings | 5 | 0 | 12-Aug-14 A | 22-Sep-14 A | |
| L03-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L06-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L08-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 11-Sep-14 A | 19-Sep-14 A | |
| L04-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| L05-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L06-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |

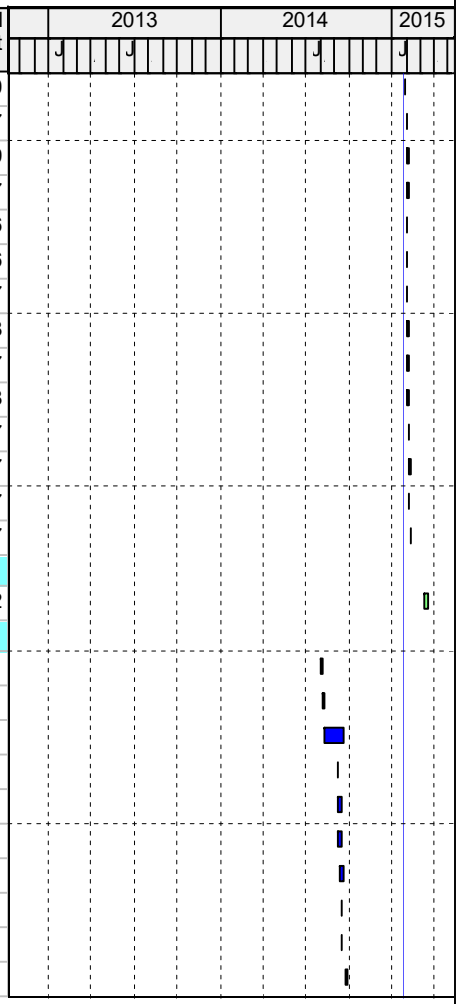


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L09-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| L10-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 08-Oct-14 A | |
| L11-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 10-Oct-14 A | |
| L08-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L12-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| L09-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L14-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 16-Oct-14 A | 27-Oct-14 A | |
| L10-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |
| L11-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L15-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 22-Oct-14 A | 29-Oct-14 A | |
| L12-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 03-Nov-14 A | 04-Nov-14 A | |
| L14-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L15-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 05-Nov-14 A | 06-Nov-14 A | |
| L16-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 14-Nov-14 A | 20-Nov-14 A | |
| L16-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L17-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L17-8200 | Wall coverings - vinyl at window niches & outside bath | 4 | 2 | 15-Dec-14 A | 27-Jan-15 | 28 |
| L04-8206 | Flooring - carpet at corridors | 2 | 0 | 14-Jan-15 A | 23-Jan-15 A | |
| L05-8206 | Flooring - carpet at corridors | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| L07-8206 | Flooring - carpet at corridors | 2 | 0 | 22-Jan-15 A | 23-Jan-15 A | |
| L06-8206 | Flooring - carpet at corridors | 2 | 2 | 26-Jan-15 | 27-Jan-15 | 23 |
| L08-8206 | Flooring - carpet at corridors | 2 | 2 | 28-Jan-15 | 29-Jan-15 | 23 |
| L04-8208 | Final clean (entire floor) | 2 | 2 | 29-Jan-15 | 30-Jan-15 | 30 |
| L05-8208 | Final clean (entire floor) | 2 | 2 | 29-Jan-15 | 30-Jan-15 | 30 |
| L09-8206 | Flooring - carpet at corridors | 2 | 2 | 30-Jan-15 | 02-Feb-15 | 23 |
| L10-8206 | Flooring - carpet at corridors | 2 | 2 | 30-Jan-15 | 02-Feb-15 | 23 |

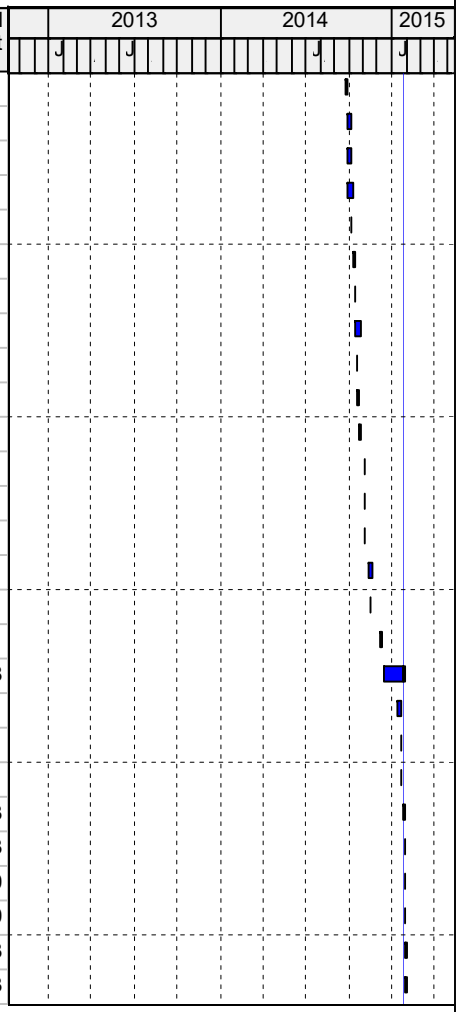


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 30 |
| L05-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 30 |
| L06-8208 | Final clean (entire floor) | 2 | 2 | 02-Feb-15 | 03-Feb-15 | 28 |
| L07-8208 | Final clean (entire floor) | 2 | 2 | 02-Feb-15 | 03-Feb-15 | 28 |
| L08-8208 | Final clean (entire floor) | 2 | 2 | 02-Feb-15 | 03-Feb-15 | 28 |
| L04-8212 | Resolve Final Punchlist | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 30 |
| L05-8212 | Resolve Final Punchlist | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 30 |
| L11-8206 | Flooring - carpet at corridors | 2 | 2 | 03-Feb-15 | 04-Feb-15 | 23 |
| L06-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 04-Feb-15 | 04-Feb-15 | 28 |
| L07-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 04-Feb-15 | 04-Feb-15 | 28 |
| L08-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 04-Feb-15 | 04-Feb-15 | 28 |
| L09-8208 | Final clean (entire floor) | 2 | 2 | 04-Feb-15 | 05-Feb-15 | 26 |
| L10-8208 | Final clean (entire floor) | 2 | 2 | 04-Feb-15 | 05-Feb-15 | 26 |
| L04-8214 | Floor Complete | 0 | 0 | | 04-Feb-15 | 30 |
| L05-8214 | Floor Complete | 0 | 0 | | 04-Feb-15 | 30 |
| L06-8212 | Resolve Final Punchlist | 2 | 2 | 05-Feb-15 | 06-Feb-15 | 28 |
| L07-8212 | Resolve Final Punchlist | 2 | 2 | 05-Feb-15 | 06-Feb-15 | 28 |
| L08-8212 | Resolve Final Punchlist | 2 | 2 | 05-Feb-15 | 06-Feb-15 | 28 |
| L12-8206 | Flooring - carpet at corridors | 2 | 2 | 05-Feb-15 | 06-Feb-15 | 23 |
| L09-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 06-Feb-15 | 06-Feb-15 | 26 |
| L10-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 06-Feb-15 | 06-Feb-15 | 26 |
| L11-8208 | Final clean (entire floor) | 2 | 2 | 06-Feb-15 | 09-Feb-15 | 41 |
| L06-8214 | Floor Complete | 0 | 0 | | 06-Feb-15 | 28 |
| L07-8214 | Floor Complete | 0 | 0 | | 06-Feb-15 | 28 |
| L08-8214 | Floor Complete | 0 | 0 | | 06-Feb-15 | 28 |
| L09-8212 | Resolve Final Punchlist | 2 | 2 | 09-Feb-15 | 10-Feb-15 | 26 |
| L10-8212 | Resolve Final Punchlist | 2 | 2 | 09-Feb-15 | 10-Feb-15 | 26 |

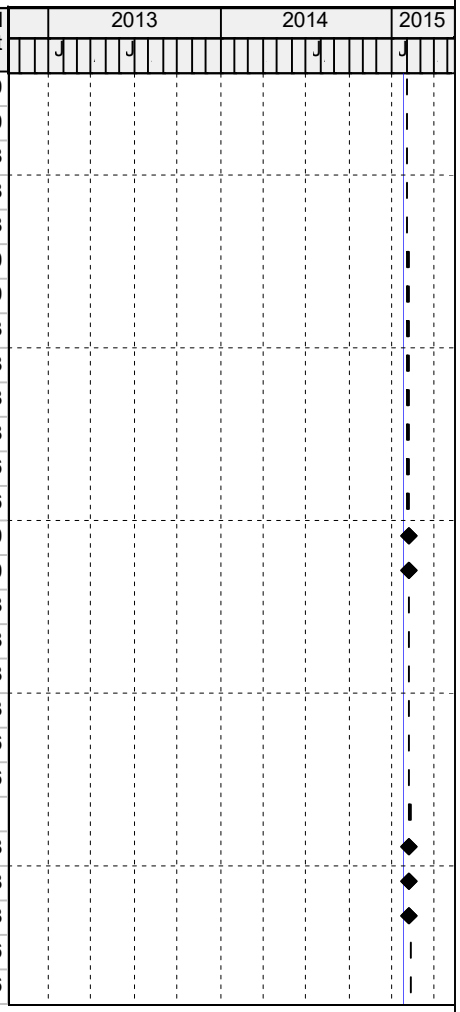



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8206 | Flooring - carpet at corridors | 2 | 2 | 09-Feb-15 | 10-Feb-15 | 31 |
| L11-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 10-Feb-15 | 10-Feb-15 | 41 |
| L12-8208 | Final clean (entire floor) | 2 | 2 | 10-Feb-15 | 11-Feb-15 | 39 |
| L09-8214 | Floor Complete | 0 | 0 | | 10-Feb-15 | 26 |
| L10-8214 | Floor Complete | 0 | 0 | | 10-Feb-15 | 26 |
| L11-8212 | Resolve Final Punchlist | 2 | 2 | 11-Feb-15 | 12-Feb-15 | 41 |
| L14-8208 | Final clean (entire floor) | 2 | 2 | 11-Feb-15 | 12-Feb-15 | 38 |
| L15-8206 | Flooring - carpet at corridors | 2 | 2 | 11-Feb-15 | 12-Feb-15 | 31 |
| L12-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 12-Feb-15 | 12-Feb-15 | 39 |
| L11-8214 | Floor Complete | 0 | 0 | | 12-Feb-15 | 41 |
| L12-8212 | Resolve Final Punchlist | 2 | 2 | 13-Feb-15 | 16-Feb-15 | 39 |
| L14-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 13-Feb-15 | 13-Feb-15 | 38 |
| L16-8206 | Flooring - carpet at corridors | 2 | 2 | 13-Feb-15 | 16-Feb-15 | 31 |
| L14-8212 | Resolve Final Punchlist | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 38 |
| L15-8208 | Final clean (entire floor) | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 38 |
| L12-8214 | Floor Complete | 0 | 0 | | 16-Feb-15 | 39 |
| L17-8206 | Flooring - carpet at corridors | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 31 |
| L14-8214 | Floor Complete | 0 | 0 | | 17-Feb-15 | 38 |
| L15-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 18-Feb-15 | 18-Feb-15 | 38 |
| L16-8208 | Final clean (entire floor) | 2 | 2 | 18-Feb-15 | 19-Feb-15 | 33 |
| L15-8212 | Resolve Final Punchlist | 2 | 2 | 19-Feb-15 | 20-Feb-15 | 38 |
| L16-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 20-Feb-15 | 20-Feb-15 | 33 |
| L17-8208 | Final clean (entire floor) | 2 | 2 | 20-Feb-15 | 23-Feb-15 | 31 |
| L15-8214 | Floor Complete | 0 | 0 | | 20-Feb-15 | 38 |
| L16-8212 | Resolve Final Punchlist | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 33 |
| L17-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 24-Feb-15 | 24-Feb-15 | 31 |
| L16-8214 | Floor Complete | 0 | 0 | | 24-Feb-15 | 33 |

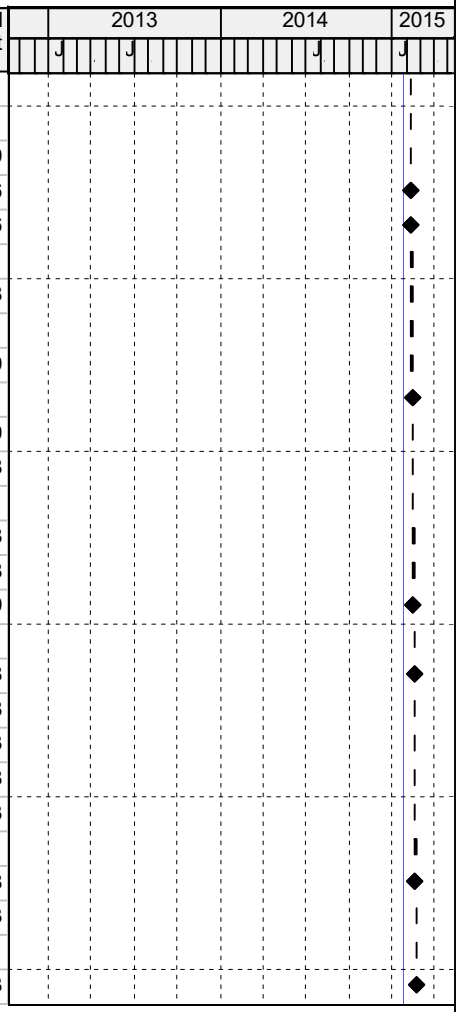



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8212 | Resolve Final Punchlist | 2 | 2 | 25-Feb-15 | 26-Feb-15 | 31 |
| L17-8214 | Floor Complete | 0 | 0 | | 26-Feb-15 | 31 |
| L03-8206 | Flooring - carpet at corridors | 2 | 2 | 30-Mar-15 | 31-Mar-15 | 2 |
| L03-8208 | Final clean (entire floor) | 2 | 2 | 02-Apr-15 | 03-Apr-15 | 2 |
| L03-8210 | Owner Walk / Create Final Punchlist | 1 | 1 | 02-Apr-15 | 02-Apr-15 | 2 |
| L03-8212 | Resolve Final Punchlist | 5 | 5 | 03-Apr-15 | 09-Apr-15 | 2 |
| L03-8214 | Floor Complete | 0 | 0 | | 09-Apr-15 | 2 |
| **Mech Penthouse** | | | | | | |
| PH-8100 | PH - Insulation & Vapor Barrier | 5 | 0 | 09-Oct-14 A | 13-Oct-14 A | |
| PH-8102 | PH - Complete GWB Hang / Tape / Finish | 6 | 0 | 14-Oct-14 A | 10-Nov-14 A | |
| PH-8122 | PH - Plumbing Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8110 | PH - HVAC Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8126 | PH - install doors & hardware | 2 | 1 | 24-Nov-14 A | 26-Jan-15 | 52 |
| PH-8104 | PH - Int Painting [DELETED] | 4 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| PH-8108 | PH - Elec Trim / Finish | 5 | 0 | 01-Dec-14 A | 19-Jan-15 A | |
| PH-8114 | PH - Install Stairs to Roof [DELETED] | 1 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| PH-8118 | PH - Fire Alarm Trim (speaker/strobe & smoke detecto | 5 | 0 | 01-Dec-14 A | 21-Jan-15 A | |
| PH-8124 | PH - Flooring [DELETED, NIC] | 5 | 0 | 01-Jan-15 A | 01-Jan-15 A | |
| PH-8132 | PH - Contractor Pre-Punchlist | 1 | 1 | 27-Jan-15 | 27-Jan-15 | 54 |
| PH-8134 | PH - Final Trims and Touch-Up | 3 | 3 | 27-Jan-15 | 29-Jan-15 | 52 |
| PH-8208 | PH - Final Clean | 1 | 1 | 30-Jan-15 | 30-Jan-15 | 52 |
| PH-8212 | PH - Final Punchlist | 1 | 1 | 02-Feb-15 | 02-Feb-15 | 52 |
| PH-8214 | PH - Floor Complete | 0 | 0 | | 02-Feb-15 | 52 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| **Smoke Control** | | | | | | |
| CO-7104 | Smoke Control Pre-Testing (Podium) | 5 | 5 | 03-Apr-15 | 09-Apr-15 | 9 |

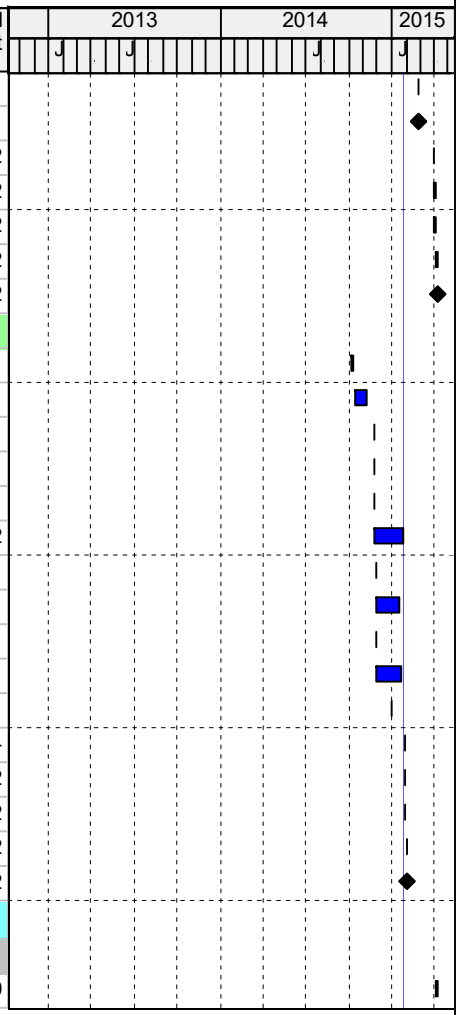


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7106 | City of Bellevue Smoke Control Testing (Podium) | 5 | 5 | 21-Apr-15 | 27-Apr-15 | 2 |
| CO-7108 | Final Marriott Smoke Control Testing | 5 | 5 | 30-Apr-15 | 07-May-15 | 0 |
| **Fire Sprinklers** | | | | | | |
| CO-7110 | Fire Sprinkler Pre-Testing (Podium) | 5 | 5 | 27-Mar-15 | 02-Apr-15 | 9 |
| CO-7112 | City of Bellevue Fire Sprinkler Inspection / Approval (F | 5 | 5 | 21-Apr-15 | 27-Apr-15 | 2 |
| CO-7114 | Marriott Fire Sprinkler Testing | 5 | 5 | 30-Apr-15 | 07-May-15 | 0 |
| **Fire Alarm** | | | | | | |
| CO-7116 | Fire Alarm Pre-Testing (Podium) | 5 | 5 | 27-Mar-15 | 02-Apr-15 | 9 |
| CO-7118 | City of Bellevue Fire Alarm Inspection / Approval (Pod | 5 | 5 | 21-Apr-15 | 27-Apr-15 | 2 |
| CO-7120 | Marriott Fire Alarm Testing | 5 | 5 | 30-Apr-15 | 07-May-15 | 0 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| CO-7100 | Cx - Start-Up - Garage Exhaust Fan and VFD's | 4 | 4 | 26-Jan-15* | 29-Jan-15 | 37 |
| CO-7102 | Cx - DDC Point-To-Point - Garage Exhaust Fans | 5 | 5 | 30-Jan-15 | 05-Feb-15 | 59 |

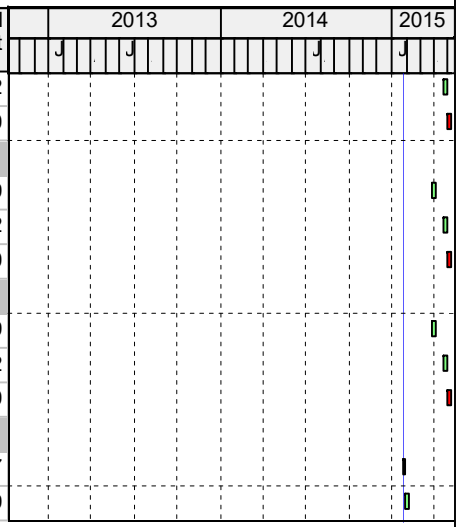



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Working Schedule - 2-16-15 Update** | | | | | | |
| L09-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-04 A | 30-Sep-14 A | |
| I-4500 | Re-design building exterior (change from EIFS panels | 30 | 0 | 12-Apr-13 A | 28-May-14 A | |
| I-1500 | Owner release revised LV design - Tower (ASIs 5, 13, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-1550 | Owner release revised LV design - Podium (ASIs 5, 1 | 200 | 0 | 23-May-13 A | 28-Apr-14 A | |
| I-1900 | Owner issue design revisions (ASIs 4, 9, 19, 34) | 215 | 0 | 23-May-13 A | 24-Mar-14 A | |
| I-2500 | Owner issue LL1 electrical revisions (ASIs 7, 9r2, 14, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-3400 | Owner provide Level 2 ceiling heights | 180 | 0 | 24-Jun-13 A | 24-Mar-14 A | |
| I-3700 | Owner resolve wall condition between stair and Eleva | 200 | 0 | 27-Jun-13 A | 16-Jun-14 A | |
| MM-1000 | MM - Temporary Power Available | 0 | 0 | 08-Jul-13 A | | |
| I-2100 | Owner revise roof steel design (Submittals 365, 370, | 200 | 0 | 09-Jul-13 A | 07-Apr-14 A | |
| I-2200 | Owner resolve elevator steel issue (RFI 112, RFI 112. | 200 | 0 | 09-Jul-13 A | 03-Mar-14 A | |
| I-2400 | Owner provide Tower light fixture selections (ASI 36) | 185 | 0 | 18-Jul-13 A | 08-Apr-14 A | |
| I-2900 | Owner revise Food Service and Kitchen (ASIs 11, 12, | 140 | 0 | 08-Aug-13 A | 27-Feb-14 A | |
| I-1400 | Owner develop envelope redesign | 70 | 0 | 27-Aug-13 A | 12-Dec-13 A | |
| I-3600 | Owner closeout glass/glazing allowance | 160 | 0 | 04-Sep-13 A | 30-Apr-14 A | |
| I-1200 | Owner release revised Concierge Lounge design (AS | 160 | 0 | 06-Sep-13 A | 08-Apr-14 A | |
| I-2800 | Owner revise interior public space design (ASIs 16, 1 | 130 | 0 | 25-Sep-13 A | 09-Apr-14 A | |
| I-2000 | Owner approve door frames (Submittals 258, 454, 48 | 85 | 0 | 27-Sep-13 A | 23-Jan-14 A | |
| I-3100 | Owner revise ballroom ceiling design (ASIs 18, 25) | 100 | 0 | 17-Oct-13 A | 25-Feb-14 A | |
| I-1600 | Owner provide directive for south & east corridor encl | 110 | 0 | 28-Oct-13 A | 18-Apr-14 A | |
| I-2300 | Owner resolve fire smoke dampers issue (RFI 233) | 115 | 0 | 30-Oct-13 A | 11-Apr-14 A | |
| I-2600 | Owner resolve L2 slab coordination issue | 4 | 0 | 13-Nov-13 A | 16-Nov-13 A | |
| I-2700 | Owner revise tower guest rooms design (ASIs 23, 29) | 58 | 0 | 04-Dec-13 A | 26-Feb-14 A | |
| I-1700 | Owner provide design for dry site utilities (ASIs 20, 20 | 66 | 0 | 09-Dec-13 A | 13-Mar-14 A | |
| I-1402 | Begin exterior panel production | 41 | 0 | 13-Dec-13 A | 12-Feb-14 A | |
| I-1300 | Owner issue "Hold" directive (email) | 0 | 0 | | 19-Dec-13 A | |

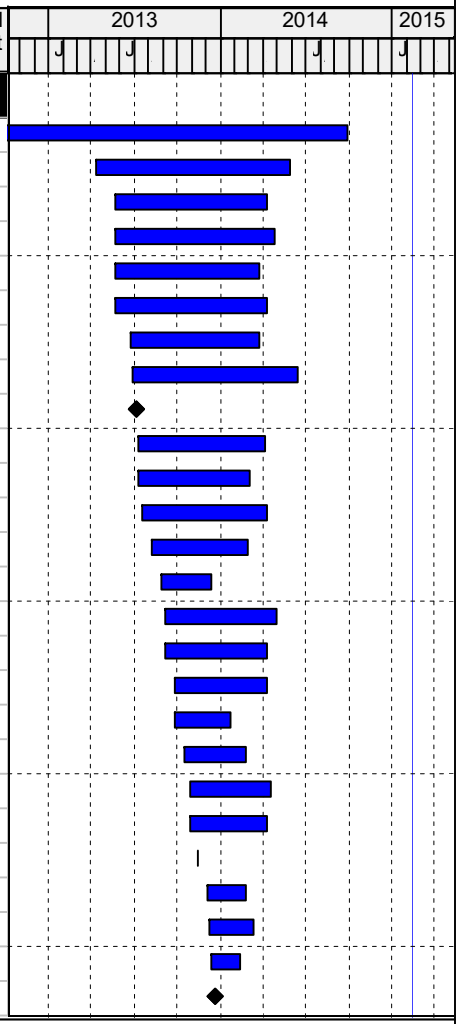


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1100 | Owner release revised L17 design (ASI 23, 29R1) | 74 | 0 | 20-Dec-13 A | 08-Apr-14 A | |
| I-1302 | Owner issue ASI 30 (Prep Kitchen Revisions) | 47 | 0 | 20-Dec-13 A | 27-Feb-14 A | |
| I-1404 | City of Bellevue Approval | 90 | 0 | 23-Dec-13 A | 15-Jul-14 A | |
| I-5470 | Resolve ceiling height issue at Laundry Room (RFI __ | 5 | 0 | 05-Jan-14 A | 30-Jan-15 A | |
| I-3000 | Owner revise bar area (change to straight bar, IDRFI-( | 71 | 0 | 22-Jan-14 A | 27-May-14 A | |
| I-1306 | Prep Kitchen - Additional plumbing (ASI 30) | 4 | 0 | 17-Feb-14 A | 01-Aug-14 A | |
| I-2202 | Fabricate revised elevator steel | 60 | 0 | 04-Mar-14 A | 07-May-14 A | |
| I-2704 | Framing "Go Back" work for ASIs 23, 29 - L4 | 1 | 0 | 05-Mar-14 A | 12-Mar-14 A | |
| I-3900 | RFI 471, Resolve Ballroom parapet height issue | 1 | 0 | 08-Mar-14 A | 07-May-14 A | |
| I-1702 | Owner provide directive to proceed | 26 | 0 | 14-Mar-14 A | 01-May-14 A | |
| I-3300 | Owner provide Guest Room plumbing fixture selectio | 1 | 0 | 20-Mar-14 A | 20-Mar-14 A | |
| I-1902 | Procure revised structural steel | 15 | 0 | 25-Mar-14 A | 14-Apr-14 A | |
| I-4000 | Owner complete design of east stitched enclosure (fo | 1 | 0 | 01-Apr-14 A | 14-May-14 A | |
| I-2102 | Fabricate revised roof steel | 20 | 0 | 08-Apr-14 A | 15-May-14 A | |
| I-3200 | Owner provide light fixture selections for podium level | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| I-3800 | Resolve  Heat Pump Electrical Overcurrent Issue | 20 | 0 | 23-Apr-14 A | 18-Jun-14 A | |
| L10-8221 | HVAC Risers Duct Insulation | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L11-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| I-2304 | Framing "Go Back" work at L3 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2306 | Framing "Go Back" work at L4 for RFI 233 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2308 | Framing "Go Back" work at L5 for RFI 233 | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2706 | Framing "Go Back" work for ASIs 23, 29 - L5 | 1 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2708 | Framing "Go Back" work for ASIs 23, 29 - L6 | 1 | 0 | 29-Apr-14 A | 09-May-14 A | |
| I-2702 | Framing "Go Back" work for ASIs 23, 29 - L3 | 1 | 0 | 01-May-14 A | 01-May-14 A | |
| I-1706 | PSE scheduling delay | 10 | 0 | 01-May-14 A | 20-May-14 A | |
| I-3602 | Complete shop drawings & fab/deliver storefront fram | 40 | 0 | 01-May-14 A | 14-Jun-14 A | |

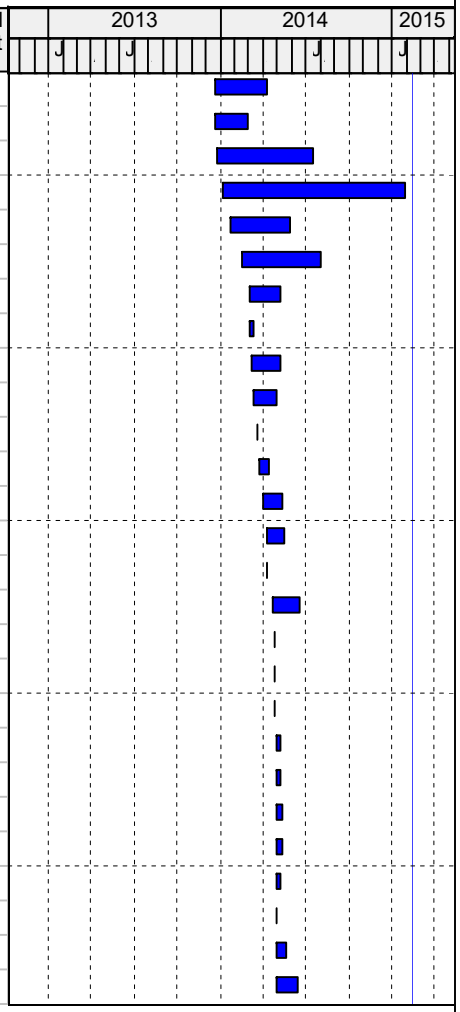


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| I-1802 | Rework framing for door hold-opens - LL4 | 1 | 0 | 07-May-14 A | 08-May-14 A | |
| L04-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-May-14 A | 12-May-14 A | |
| I-1800 | Owner issue directive to proceed with door hold-open | 1 | 0 | 08-May-14 A | 08-May-14 A | |
| I-1804 | Rework framing for door hold-opens - LL3 | 1 | 0 | 08-May-14 A | 09-May-14 A | |
| I-2312 | Framing "Go Back" work at L7 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-2314 | Framing "Go Back" work at L8 for RFI 233 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-3902 | Install Ballroom parapet extension | 5 | 0 | 08-May-14 A | 13-May-14 A | |
| I-1806 | Rework framing for door hold-opens - LL2 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-1808 | Rework framing for door hold-opens - LL1 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-2310 | Framing "Go Back" work at L6 for RFI 233 | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| I-2710 | Framing "Go Back" work for ASIs 23, 29 - L7 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| L05-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L06-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L05-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| LL2E-8110 | LL2 - Electrical, Fire pumps/equipment final connectic | 5 | 0 | 12-May-14 A | 30-Oct-14 A | |
| PH-8704 | PH - Install Machine Support Steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| PH-8710 | Install elevator rail support steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| L03-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L03-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 13-May-14 A | 14-May-14 A | |
| I-4002 | East Stitched - Install framing and windows | 9 | 0 | 19-May-14 A | 09-Jun-14 A | |
| L10-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L11-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L12-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| RF-4038 | AR - Concrete pads and curbs | 5 | 0 | 21-May-14 A | 04-Jun-14 A | |
| L10-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |

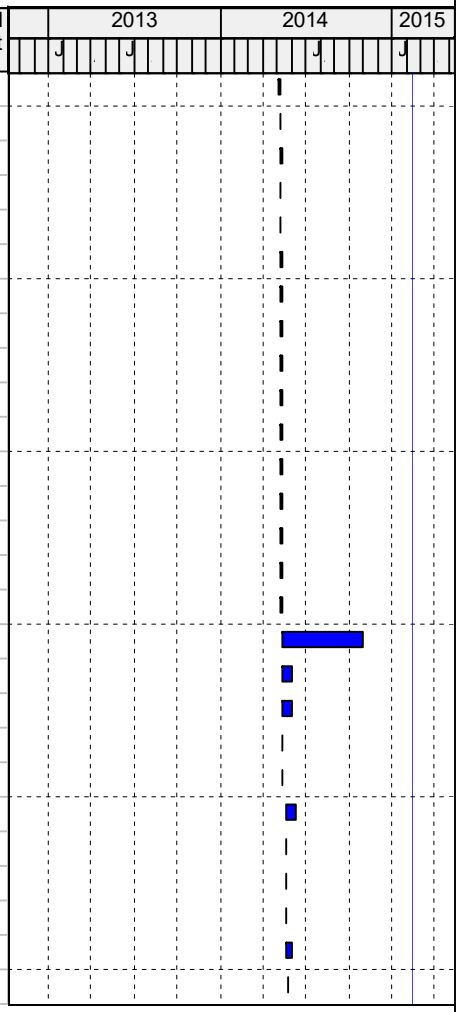



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L12-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L14-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L15-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 27-May-14 A | |
| L11-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 07-Jun-14 A | |
| L12-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 27-May-14 A | 06-Jun-14 A | |
| I-3002 | City of Bellevue approve bar design changes. | 5 | 0 | 28-May-14 A | 12-Dec-14 A | |
| I-4502 | Release metal panels for fabrication | 0 | 0 | 28-May-14 A | | |
| I-4504 | Metal panel fabrication (1st delivery) | 1 | 0 | 29-May-14 A | 08-Jul-14 A | |
| L16-8221 | HVAC Risers Duct Insulation | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| PH-8712 | PH - Complete Framing and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| PH-8714 | Stage PH/L18 roofing materials | 2 | 0 | 30-May-14 A | 30-May-14 A | |
| L08-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L08-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 02-Jun-14 A | 20-Jun-14 A | |
| PH-8704I | Correct support steel embeds | 2 | 0 | 02-Jun-14 A | 11-Jun-14 A | |
| L14-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 03-Jun-14 A | 04-Jun-14 A | |
| L17-8221 | HVAC Risers Duct Insulation | 1 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| PC-4010 | PC - Fireproof Entry Roof Steel | 5 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| I-4100 | Owner resolve trap primers issue (RFI 560) | 5 | 0 | 03-Jun-14 A | 20-Jun-14 A | |
| RF-6028 | Tower Roof - Structural Steel | 5 | 0 | 04-Jun-14 A | 17-Jun-14 A | |
| L14-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |

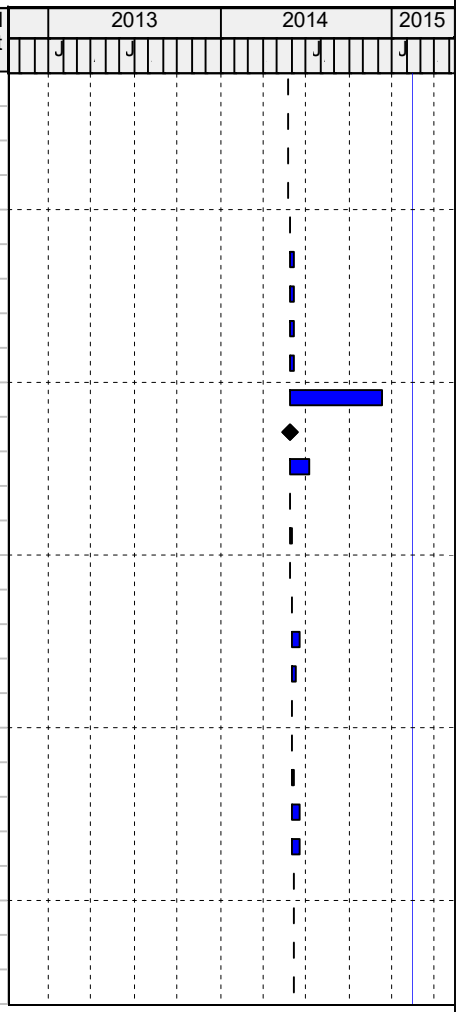



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L1B-6005 | Head of Wall Fire Caulk at CMU (including East Servi | 2 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L14-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L15-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L16-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L09-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 11-Jun-14 A | 12-Jun-14 A | |
| I-3702 | Complete wall framing at Stair/Elevator 5 (LL4) | 2 | 0 | 18-Jun-14 A | 20-Jun-14 A | |
| I-3720 | Fireproof added steel between Stair 1 and Elevator 5 | 5 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| I-3722 | Complete GWB between Stair 1 and Elevator 5 shaft | 10 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| LL1-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 22-Jul-14 A | |
| TC-5912 | Tower Crane pour-backs (LL4 to L3) | 4 | 0 | 19-Jun-14 A | 26-Jun-14 A | |
| LL1-Z2-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL4-6005 | LL4 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| LL3-6005 | LL3 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| L03-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 21-Jun-14 A | 21-Jun-14 A | |
| L06-6040 | Test Heat Pumps - L3, L4, L5 and L6 | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L03-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| L17-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL2-6005 | LL2 - Seismic Head Of Wall Fire Caulk at CMU | 5 | 0 | 24-Jun-14 A | 18-Jul-14 A | |
| I-3704 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL1-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z2-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z3-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 04-Aug-14 A | |
| L1L-6005 | Head of Wall Fire Caulk at CMU (including back of ho | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1K-6005 | Head of Wall Fire Caulk at CMU & Inspection | 2 | 0 | 24-Jun-14 A | 08-Aug-14 A | |
| L03-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L04-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |

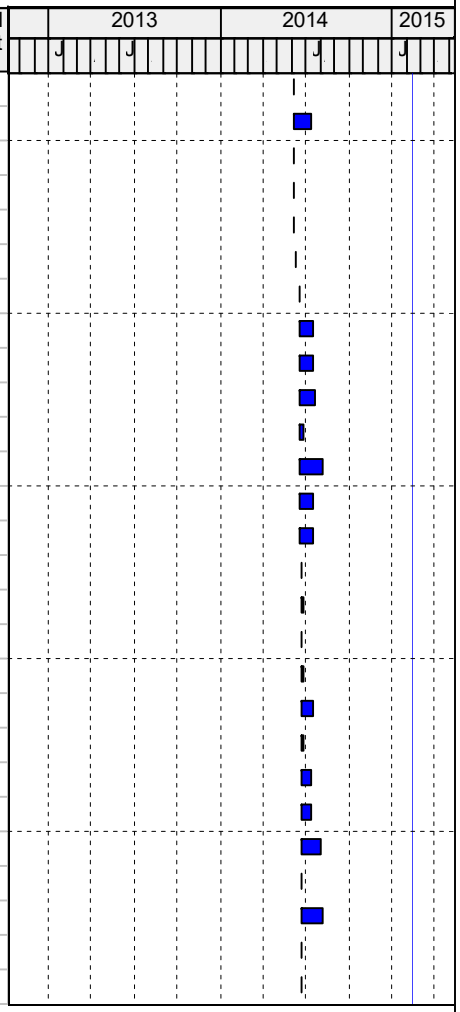



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| I-3710 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| I-3712 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| L1K-6018a | Install Kitchen hoods and grease ducts (OFCI) | 10 | 0 | 25-Jun-14 A | 07-Oct-14 A | |
| L03-8604 | L3 Pool - Plumbing R/I | 5 | 0 | 25-Jun-14 A | 10-Nov-14 A | |
| L04-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 26-Jun-14 A | 03-Jul-14 A | |
| L09-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 26-Jun-14 A | 26-Jun-14 A | |
| I-3706 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 26-Jun-14 A | 10-Jul-14 A | |
| L03-8600 | L3 Pool - Framing & HM frames | 5 | 0 | 26-Jun-14 A | 20-Nov-14 A | |
| L05-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L08-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L04-7018 | Electrical Rough-In | 1 | 0 | 27-Jun-14 A | 22-Jul-14 A | |
| L04-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 27-Jun-14 A | 23-Jul-14 A | |
| L03-7020 | HVAC Rough-In | 1 | 0 | 29-Jun-14 A | 15-Jul-14 A | |
| L1RR-8100 | Insulation [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8100 | Insulation [DELETED - included in Ballroom activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8100 | Insulation [DELETED - included in Meeting Rooms ac | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8102 | GWB Hang [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8215 | GWB Tape [DELETED - included in Meeting Rooms a | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8104 | Prime Paint [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |

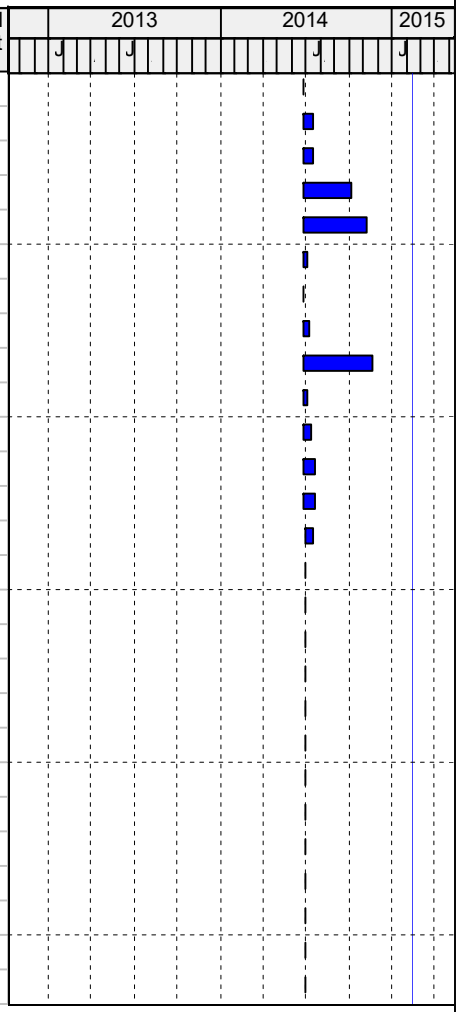


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z7-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8102 | GWB Hang [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8215 | GWB Tape [DELETED - included in Ballroom activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8104 | Prime Paint [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8102 | GWB Hang [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8215 | GWB Tape [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8104 | Prime Paint [DELETED - included in Kitchen activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L03-7018 | Electrical Rough-In | 1 | 0 | 01-Jul-14 A | 14-Jul-14 A | |
| L03-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Jul-14 A | 15-Jul-14 A | |
| L10-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7102 | Install Vertical Heat Pump | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L03-7116 | Frame Walls | 1 | 0 | 02-Jul-14 A | 14-Jul-14 A | |
| L03-7118 | Install HM Door Frame | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L04-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L05-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L07-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L08-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L09-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L10-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L12-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| I-3708 | Complete wall framing at Stair/Elevator 5 (LL3) | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |

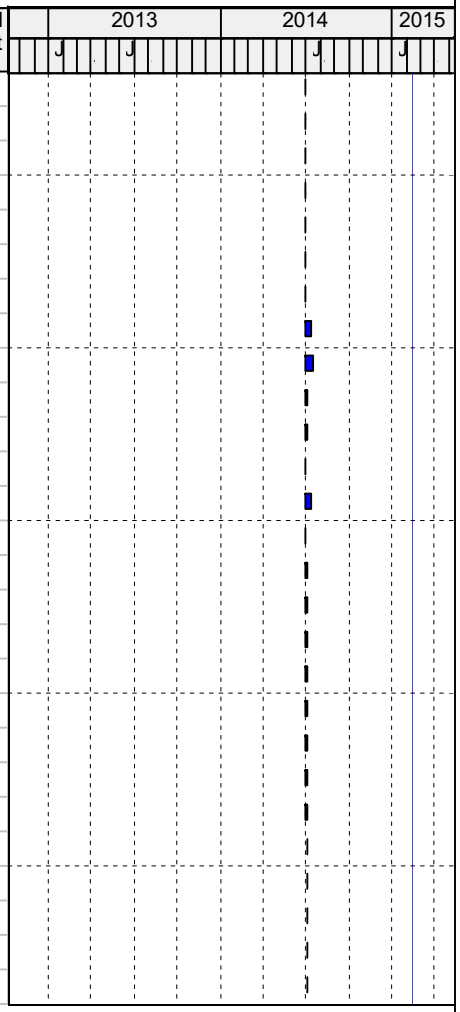



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L11-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 03-Jul-14 A | 07-Jul-14 A | |
| L04-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L05-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L06-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L07-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L08-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L17-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L10-6040 | Test Heat Pumps - L7, L8, L9 and L10 | 3 | 0 | 07-Jul-14 A | 09-Jul-14 A | |
| L10-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L03-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L04-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L05-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L06-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L07-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L08-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L09-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L10-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |

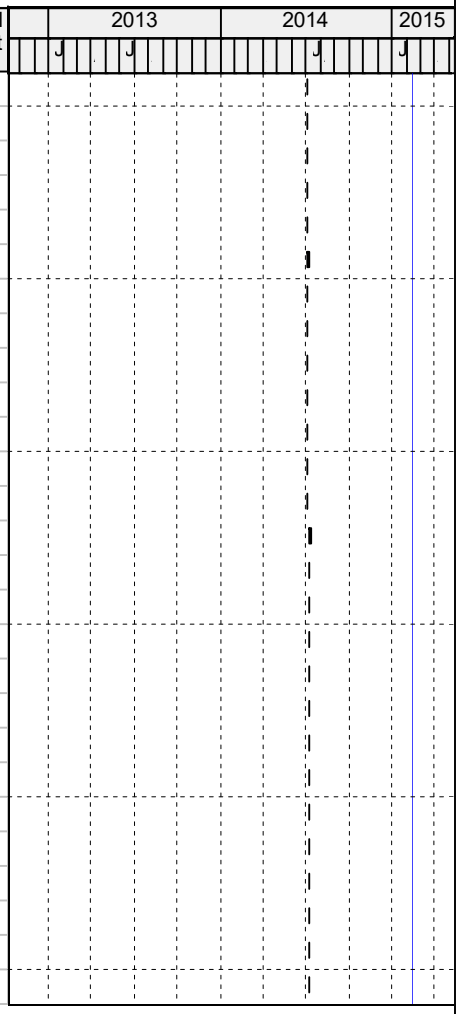



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L12-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L14-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L11-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Jul-14 A | 29-Jul-14 A | |
| L03-8602 | L3 Pool - Fire Sprinkler R/I | 5 | 0 | 08-Jul-14 A | 22-Jul-14 A | |
| L03-7016 | Install HM door frame | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L11-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L16-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 09-Jul-14 A | |
| L04-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |

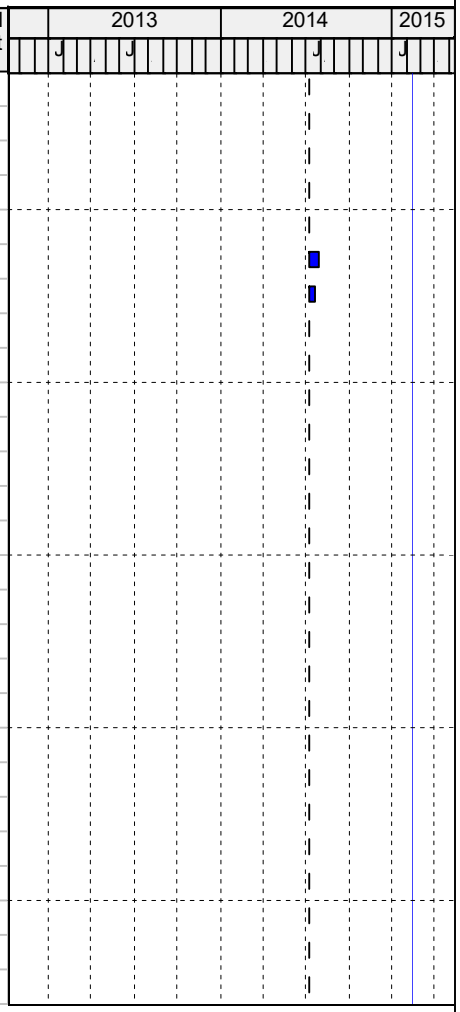



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L12-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| MP-FAB1 | Fabricate and Deliver Bronze Gold Horizontal Panels | 30 | 0 | 09-Jul-14 A | 15-Jul-14 A | |
| L04-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L05-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L06-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L16-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| MP-FAB2 | Fabricate and Deliver Silver Vertical Panels | 45 | 0 | 10-Jul-14 A | 25-Aug-14 A | |
| I-3004 | Issue ASI 38 | 0 | 0 | 11-Jul-14 A | | |
| I-3006 | Release bar area for x-ray examination | 5 | 0 | 11-Jul-14 A | 03-Sep-14 A | |
| L07-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| LL1-Z2-6018a | Complete Mech RI at tower crane opening (LL1) | 4 | 0 | 14-Jul-14 A | 17-Jul-14 A | |
| L08-6223 | Frame Corridor Ceilings | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| SW-2006a | Complete Dry Utilities (Phase 2) | 5 | 0 | 14-Jul-14 A | 24-Jul-14 A | |
| L04-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L04-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |

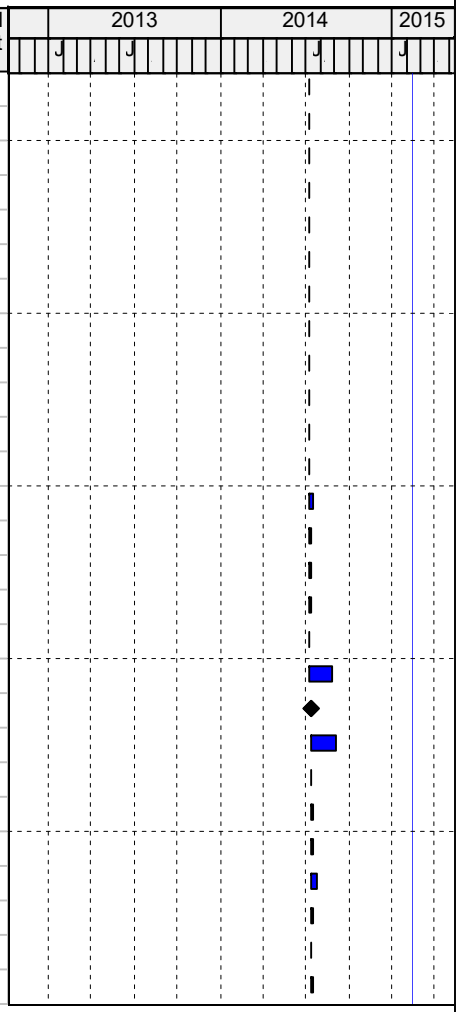



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L06-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L04-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L11-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L11-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L12-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L12-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L15-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |

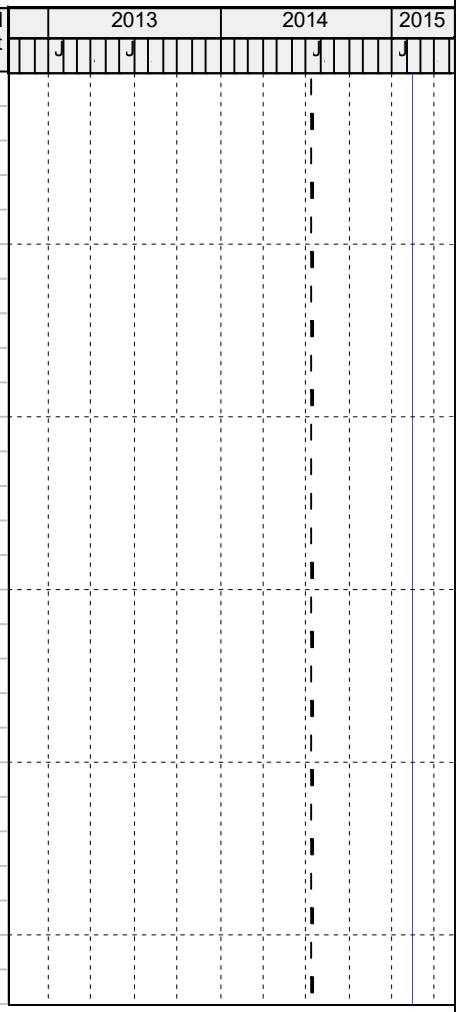



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-7102 | Install Vertical Heat Pump | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L1B-6026 | Install operable partition steel | 2 | 0 | 15-Jul-14 A | 08-Aug-14 A | |
| L09-6223 | Frame corridor ceilings | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L03-7120 | Electrical Rough-In | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L07-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L07-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L08-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L08-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L09-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L09-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L03-7142 | Install Laundry Chute (All Levels) | 9 | 0 | 15-Jul-14 A | 25-Jul-14 A | |
| LL2-2045 | LL2 - Electrical Room build-out | 15 | 0 | 15-Jul-14 A | 26-Sep-14 A | |
| L03-7122 | HVAC Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L04-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L05-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L06-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L07-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L07-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L08-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L08-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L09-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L09-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |

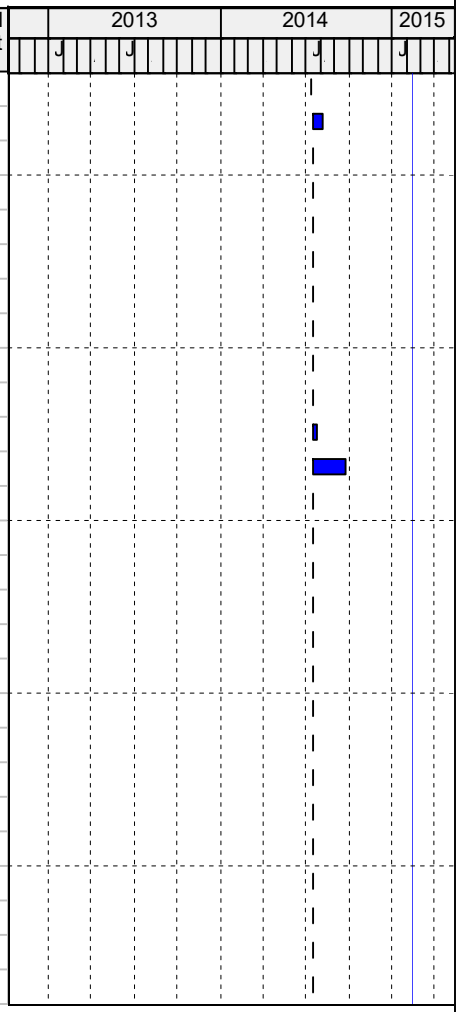



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L11-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L11-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L12-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L12-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L15-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L15-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L16-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L17-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L04-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L04-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L05-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L05-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L06-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L06-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L07-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L08-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |

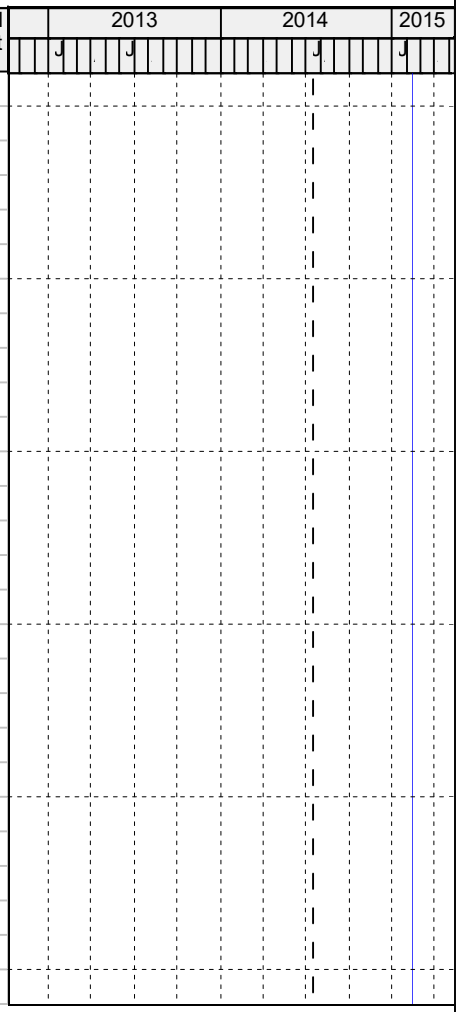



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L09-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L11-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L11-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L12-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L12-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L16-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L03-8608 | L3 Pool - Electrical R/I | 5 | 0 | 18-Jul-14 A | 10-Nov-14 A | |
| L03-8610 | L3 Pool - Fire Alarm / Elec Specialties R/I | 5 | 0 | 18-Jul-14 A | 10-Nov-14 A | |
| L15-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L15-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| L17-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L17-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| LL2-2052 | LL2 - Install fuel piping and exhaust duct to Generatc | 8 | 0 | 21-Jul-14 A | 15-Aug-14 A | |
| L04-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L04-7016 | Install HM door frame | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L07-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |

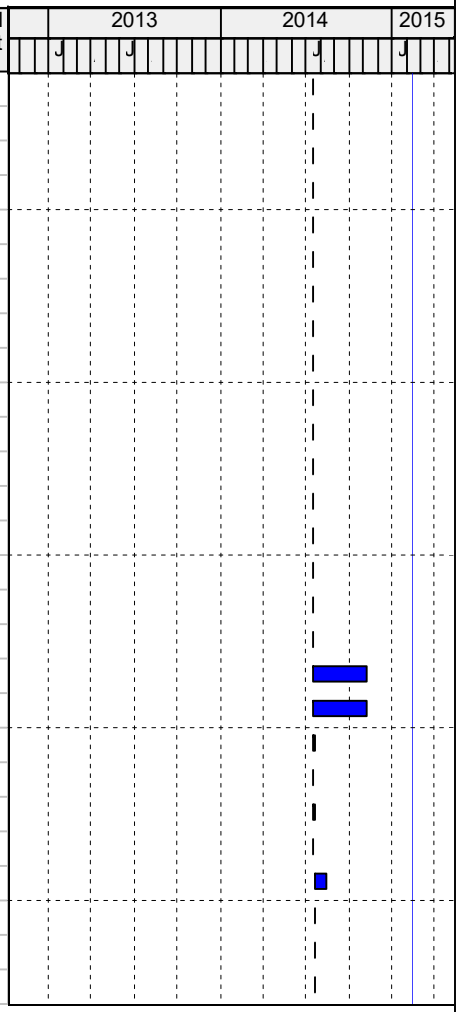


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L10-7116 | Frame Walls | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L16-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 21-Jul-14 A | 22-Jul-14 A | |
| L16-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L17-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| MPT-1002 | Tower - Install Elevation 35 (east elevation-south half) | 8 | 0 | 25-Jul-14 A | 04-Aug-14 A | |
| L16-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 25-Jul-14 A | 25-Jul-14 A | |
| L11-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L14-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L15-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L16-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L10-6223 | Frame Corridor Ceilings | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L11-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L15-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L15-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L11-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L14-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L16-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| I-1304 | Prep Kitchen - Additional framing (ASI 30) | 2 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-2302 | Framing "Go Back" work at LL1 for RFI 233 | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| I-2502 | Electrical rework at LL1 for ASIs 7, 9r2, 14, 27 | 4 | 0 | 01-Aug-14 A | 08-Aug-14 A | |

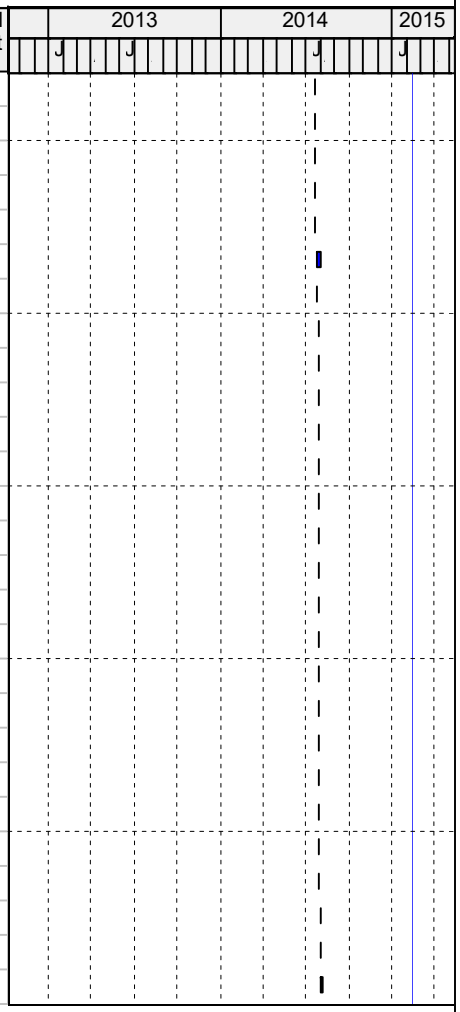



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L1B-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 01-Aug-14 A | 15-Aug-14 A | |
| MPL4-1000 | Upper L4 Ballroom - Install Elevations 1, 2 & 3 (south | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1000 | Tower - Install Elevations 26-27 (west elevation) [DELI | 13 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPP-1002 | Podium - Install Elevations 1 & 2 (west elevation, sou | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPP-1008 | Podium - Install Elevations 7 & 8 (north & east elevati | 9 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1002 | Upper L4 Ballroom - Install Elevation 10 (west elevatic | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1004 | Upper L4 Ballroom - Install Elevation 9 (north elevatio | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1006 | Tower - Install Elevation 40 (east return-east end) [DE | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1010 | Tower - Install Elevations 51 (north elevation) [DELET | 8 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-4004 | East Stitched - Install metal panels [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L11-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L11-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L15-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L14-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L17-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| MPT-1010b | Tower - Install Elevation 45 [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L16-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 04-Aug-14 A | 05-Aug-14 A | |
| L11-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Aug-14 A | 08-Aug-14 A | |
| L04-7020 | HVAC Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |

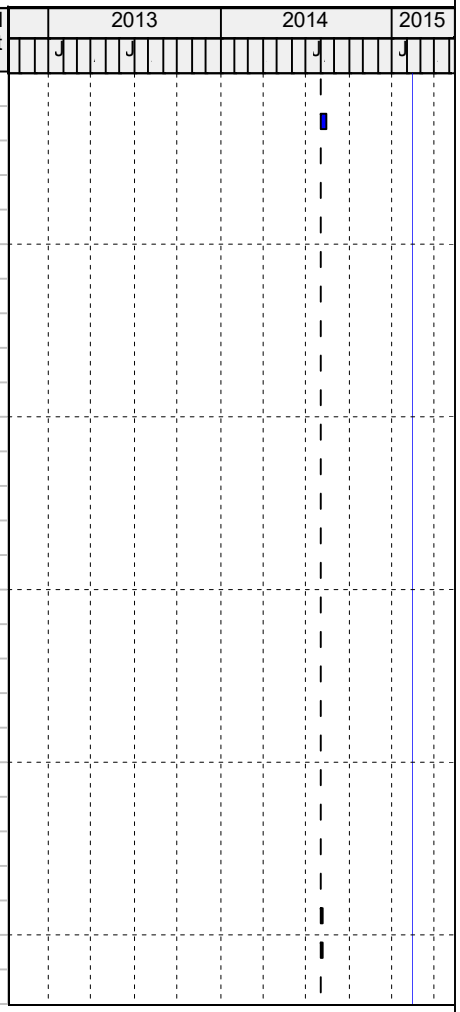



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L14-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L15-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 05-Aug-14 A | 07-Aug-14 A | |
| L05-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L06-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L07-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L08-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L09-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L10-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7018 | Electrical Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L14-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 05-Aug-14 A | 06-Aug-14 A | |
| L14-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| I-4104 | Install added trap primers - LL1 | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |

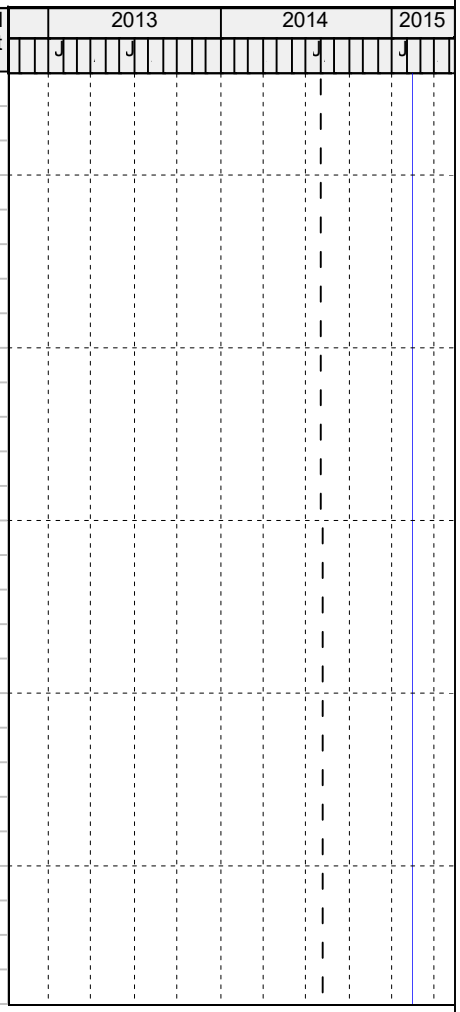



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L07-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L08-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L09-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L10-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7020 | HVAC Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L16-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| EL-1220 | Elevator fronts delivered | 0 | 0 | 07-Aug-14 A | | |
| L12-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L12-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-6223 | Frame Corridor Ceilings | 4 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L11-7016 | Install HM door frame | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L12-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L15-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L15-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L16-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L16-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |

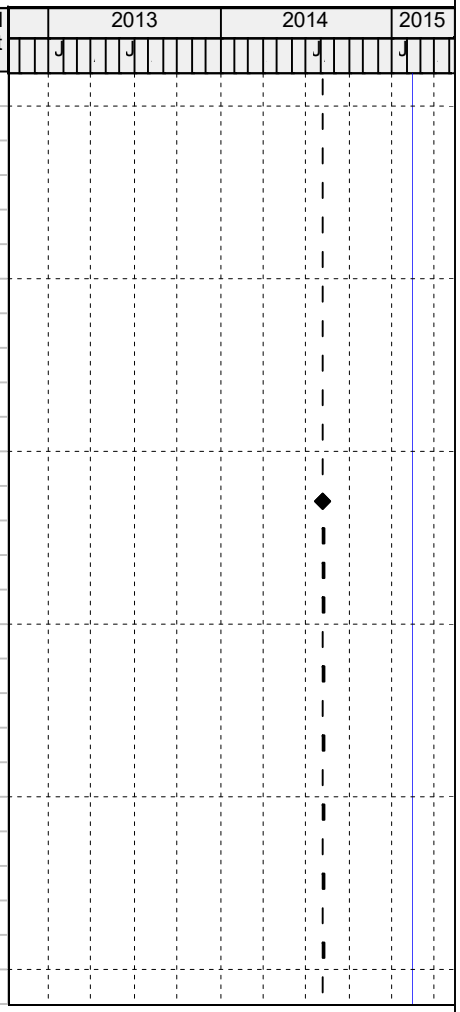



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L17-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-6040 | Test Heat Pumps - L11, L12 and L14 | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| PH-6026 | PH - Insulation/Vapor Barrier/GWB at Exterior Walls | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| L11-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L11-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-7026 | Inspections for GWB Cover | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 13-Aug-14 A | 13-Aug-14 A | |
| L15-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 14-Aug-14 A | 15-Aug-14 A | |
| LL2E-8108 | LL2 - Set fire pumps and equipment | 5 | 0 | 14-Aug-14 A | 29-Sep-14 A | |
| L10-7028 | GWB Hang/Tape/Finish | 5 | 0 | 14-Aug-14 A | 05-Dec-14 A | |
| L12-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L12-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L16-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L1BOH2-6008 | Int Wall Framing & Inspection | 5 | 0 | 14-Aug-14 A | 20-Aug-14 A | |
| I-4106 | Install added trap primers - L1 | 1 | 0 | 15-Aug-14 A | 15-Aug-14 A | |
| L14-6223 | Frame Corridor Ceilings | 4 | 0 | 15-Aug-14 A | 16-Aug-14 A | |

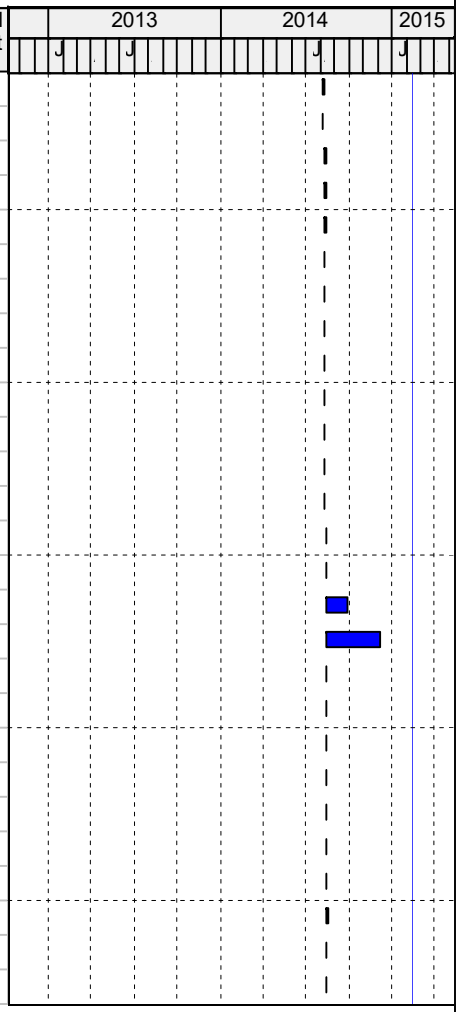



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8136 | Install Counter Subtops | 3 | 0 | 15-Aug-14 A | 18-Aug-14 A | |
| LL2-2054 | LL2 - GWB, Hang 1st Layer at Laundry Room | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| LL2E-8112 | LL2 - Form/Pour Fire Pump Pads/Curbs | 2 | 0 | 16-Aug-14 A | 18-Aug-14 A | |
| LL1-6014Ia | L1 bar redesign - rework plumbing at ceilings | 10 | 0 | 18-Aug-14 A | 05-Jan-15 A | |
| L15-6223 | Frame Corridor Ceilings | 4 | 0 | 18-Aug-14 A | 21-Aug-14 A | |
| L17-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Aug-14 A | 18-Aug-14 A | |
| L04-8136 | Install Counter Subtops | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-6014Ic | L1 bar redesign - rework electrical at ceilings | 10 | 0 | 18-Aug-14 A | 05-Jan-15 A | |
| LL2E-8114 | LL2 - Set Tube Steel at Door | 1 | 0 | 19-Aug-14 A | 19-Aug-14 A | |
| L17-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 20-Aug-14 A | 21-Aug-14 A | |
| L17-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 20-Aug-14 A | 20-Aug-14 A | |
| L05-8136 | Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 26-Aug-14 A | |
| L06-8136 | Bathrooms - Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 13-Oct-14 A | |
| L16-6223 | Frame Corridor Ceilings | 4 | 0 | 21-Aug-14 A | 29-Aug-14 A | |
| L17-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 21-Aug-14 A | 22-Aug-14 A | |
| L17-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 21-Aug-14 A | 21-Aug-14 A | |
| L1BOH2-6016 | Electrical RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6018 | HVAC RI | 4 | 0 | 21-Aug-14 A | 17-Oct-14 A | |
| L15-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7020 | HVAC Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7022 | Fire Sprinkler Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| LL2E-8116 | LL2 - Set Door Jamb | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |

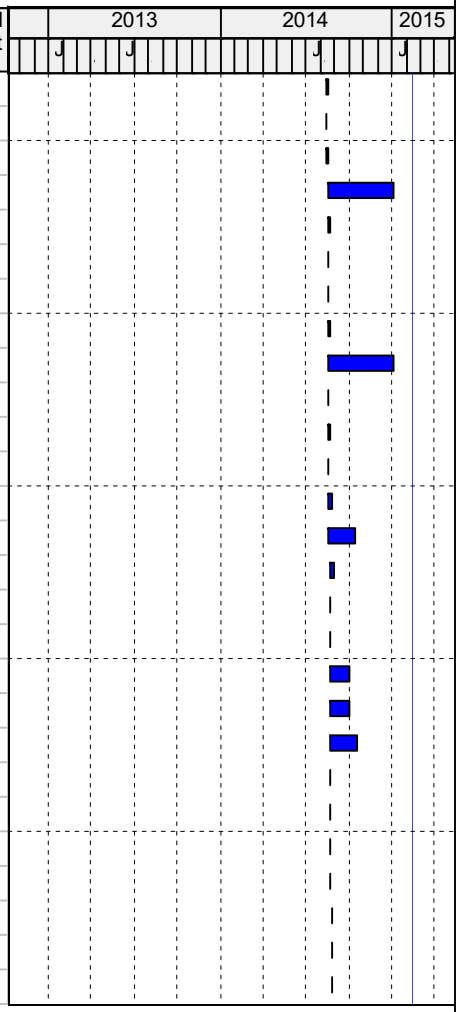



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7028 | GWB Hang/Tape/Finish | 5 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L05-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L05-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L06-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L06-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L03-8123 | Bathroom "Barn Doors" On Site | 0 | 0 | 25-Aug-14 A | | |

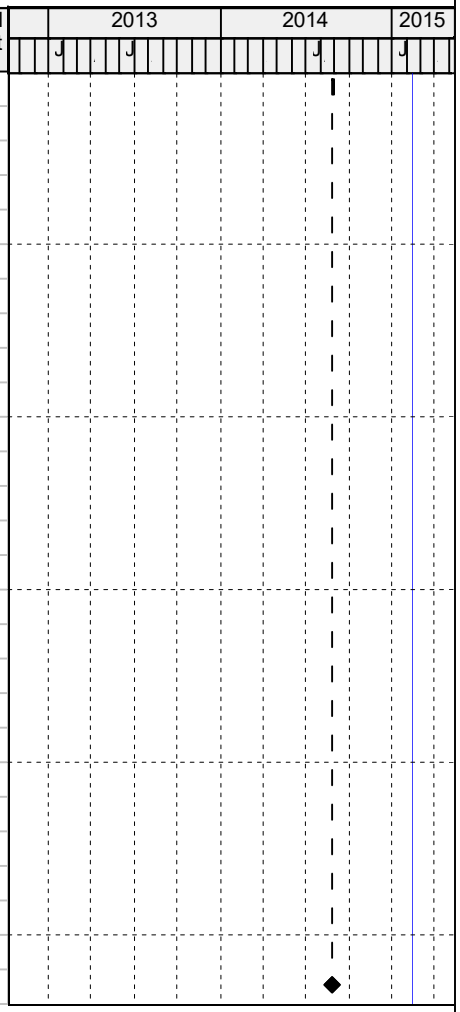



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-6026 | LL3 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL2-6026 | LL2 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL1-Z3-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L1BOH2-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L02-6026 | L2 - Set Elevator Fronts (Cars 1-4 | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L03-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L04-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L05-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L06-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L07-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L08-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L09-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L10-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L11-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L12-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L14-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L15-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L16-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L17-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| MPT-1008 | Tower - Install E/W Wing, N. Side West Half (Elev 50,: | 7 | 0 | 26-Aug-14 A | 03-Oct-14 A | |
| L06-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L07-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L08-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L05-7026 | Inspections for GWB Cover | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L05-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L11-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 08-Dec-14 A | |
| L12-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |

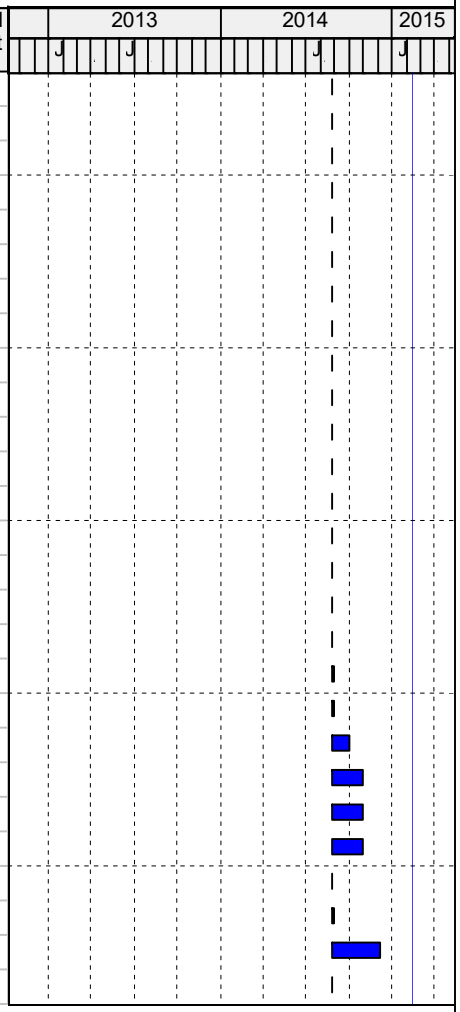



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L03-8105a | Painting - Split Door Jambs | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L09-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L10-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L11-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L12-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L14-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L15-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L16-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L05-8201 | Install ACT Grid @ Corridors | 2 | 0 | 27-Aug-14 A | 28-Aug-14 A | |
| L16-7022 | Fire Sprinkler Rough-In | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L04-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L06-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| EP-5110a | L1 - Install Steel at Revolving Door Opening | 3 | 0 | 27-Aug-14 A | 29-Aug-14 A | |
| L05-8105a | Painting - Split Door Jambs | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| I-4102 | Install added trap primers - LL2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4108 | Install added trap primers - L2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4110 | Install added trap primers - L3 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4112 | Install added trap primers - Roof PH | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| L03-8124d | Flooring On Site and Acclimated | 2 | 0 | 29-Aug-14 A | 01-Sep-14 A | |
| L02-5102 | L2 - Storefront Frames | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| L04-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L05-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L17-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L03-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L12-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L14-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |

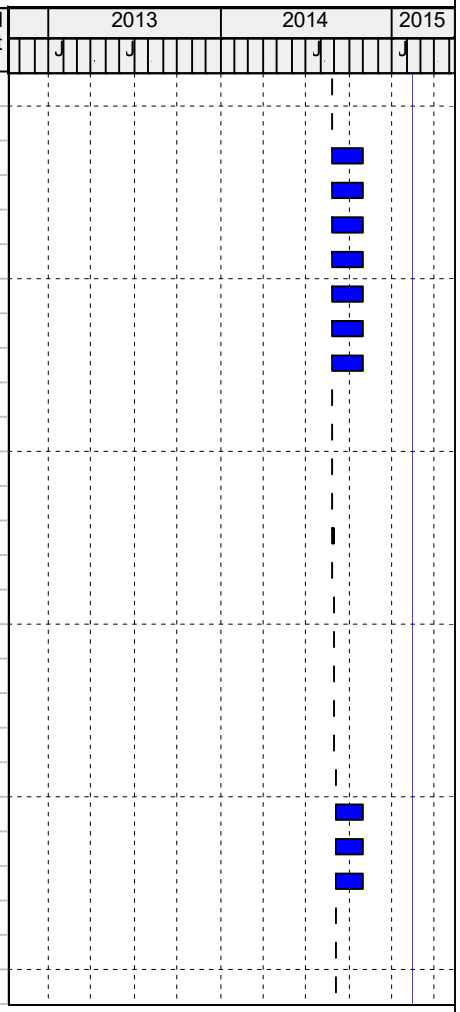



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8136 | Install Counter Subtops | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| LL1-Z3-FCC10 | FCC - Set Jamb | 1 | 0 | 02-Sep-14 A | 03-Sep-14 A | |
| MPT-1004 | Tower - Install E/W Wing, S. Side w/o Windows (Elev | 10 | 0 | 03-Sep-14 A | 17-Oct-14 A | |
| L03-7028 | GWB Hang/Tape/Finish | 5 | 0 | 03-Sep-14 A | 02-Dec-14 A | |
| L12-7028 | GWB Hang/Tape/Finish | 5 | 0 | 03-Sep-14 A | 08-Dec-14 A | |
| L03-8126a | Doors & Hardware On Site | 0 | 0 | 03-Sep-14 A | | |
| LL1-Z3-FCC12 | FCC - Sheetrock Outside Wall | 1 | 0 | 03-Sep-14 A | 03-Sep-14 A | |
| L16-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| L17-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Sep-14 A | 11-Sep-14 A | |
| L02-5104b | L2 - Install Storefront Temporary Enclosures | 1 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| LL1-Z3-FCC14 | FCC - Verify Fire Caulk OK & Inspect Room OK to 2n | 1 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| I-3008 | Coordinate and perform x-ray examination | 7 | 0 | 04-Sep-14 A | 12-Sep-14 A | |
| L02-5104a | L2 - Measure/Fabricate Storefront Glazing | 15 | 0 | 05-Sep-14 A | 18-Sep-14 A | |
| LL1-Z3-FCC16 | FCC - GWB, Hang 2nd Layer | 2 | 0 | 05-Sep-14 A | 08-Sep-14 A | |
| L03-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L15-7018 | Electrical Rough-In | 1 | 0 | 08-Sep-14 A | 08-Sep-14 A | |
| EL-1228 | Construct/Approve elevator lobby framing mockup (L | 3 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| LL2E-8118 | LL2 - Frame Infill, Install Densglass & Inspect at Fire I | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L06-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L08-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L15-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7018 | Electrical Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L3-5104a | L3 - Measure/Fabricate Storefront Glazing | 15 | 0 | 09-Sep-14 A | 30-Sep-14 A | |
| L03-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 23-Sep-14 A | |

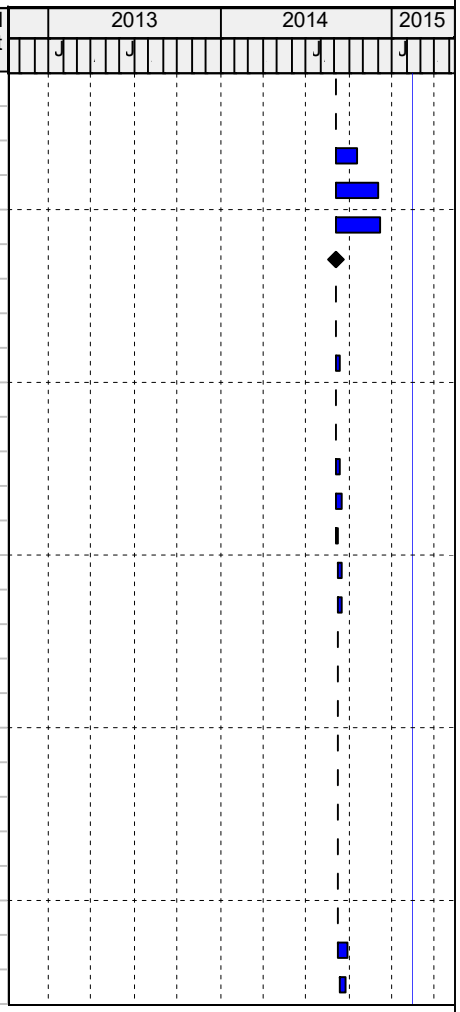



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L04-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L06-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| L08-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| L05-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L06-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L06-7028 | GWB Hang/Tape/Finish | 5 | 0 | 10-Sep-14 A | 02-Dec-14 A | |
| L08-7028 | GWB Hang/Tape/Finish | 5 | 0 | 10-Sep-14 A | 05-Dec-14 A | |
| L15-7026 | Inspections for GWB Cover | 1 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| LL2E-8120 | LL2 - Insulation, Vapor Barrier & Inspect at Fire Pump | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L08-8395 | Framing at Elevator Lobby | 4 | 0 | 11-Sep-14 A | 17-Sep-14 A | |
| L15-7028 | GWB Hang/Tape/Finish | 5 | 0 | 11-Sep-14 A | 08-Dec-14 A | |
| L08-8136 | Install Counter Subtops | 3 | 0 | 11-Sep-14 A | 16-Sep-14 A | |
| L02-6025 | L2 - Framing Go-Back Work (left out for mechanical e | 4 | 0 | 11-Sep-14 A | 02-Oct-14 A | |
| L1-5104a | L1 - Measure/Fabricate Storefront Glazing | 15 | 0 | 12-Sep-14 A | 18-Sep-14 A | |
| L1B-8102c | Finish framing and MEP at Main Ballroom East Wall ( | 10 | 0 | 12-Sep-14 A | 02-Oct-14 A | |
| L09-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L10-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L11-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L12-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L16-7026 | Inspections for GWB Cover | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| MPT-1014 | Tower - Install E/W Wing, N. Side, E. Half (Elev 46-49 | 8 | 0 | 15-Sep-14 A | 28-Oct-14 A | |
| LL2-6032 | LL2 - Complete Framing (Including Elevator Lobby) | 4 | 0 | 15-Sep-14 A | 18-Sep-14 A | |
| L1-5104b | L1 - Install Storefront Temporary Enclosures | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| LL1-Z3-FCC18 | FCC - Install Temp Door | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| LL2-2058a | LL2 - GWB Hang 1st Layer | 5 | 0 | 15-Sep-14 A | 19-Sep-14 A | |

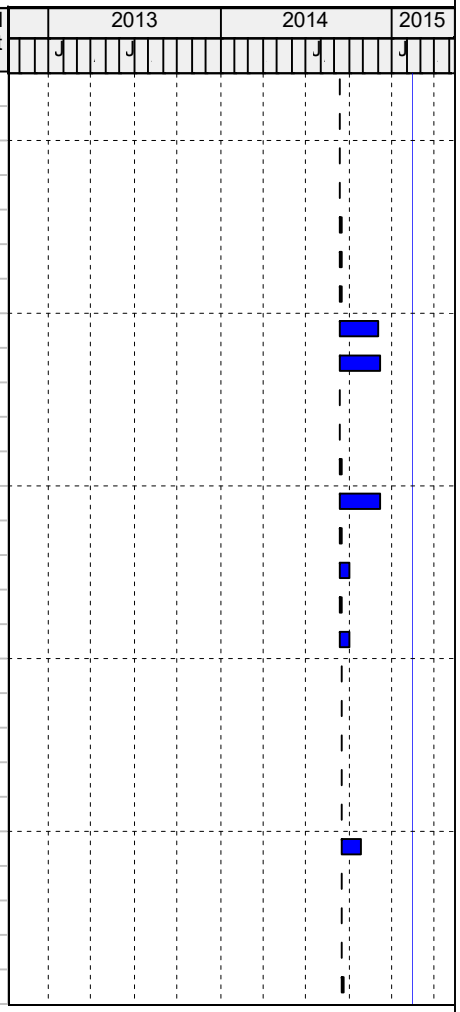



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2064 | LL2 - Generator Room - Finish Exhaust Piping | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| I-3010 | Prepare proposal for MEP relocations | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| L16-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L07-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L09-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L10-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L14-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L15-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L03-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| L16-7028 | GWB Hang/Tape/Finish | 5 | 0 | 16-Sep-14 A | 08-Dec-14 A | |
| L17-7018 | Electrical Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L09-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L10-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| LL3-6028 | LL3 - Frame Elevator Lobby | 2 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| LL4-6026 | LL4 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| I-3012 | Owner approve proposal for MEP relocations | 3 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| L11-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L12-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L14-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L15-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L04-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L17-7026 | Inspections for GWB Cover | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L17-7116 | Frame Walls | 4 | 0 | 17-Sep-14 A | 29-Sep-14 A | |
| LL2-2066 | LL2 - Generator Room - Finish Fuel Piping | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L16-8395 | Framing at Elevator Lobby | 4 | 0 | 18-Sep-14 A | 26-Sep-14 A | |
| L02-5104 | L2 - Storefront Glazing | 2 | 0 | 18-Sep-14 A | 22-Sep-14 A | |

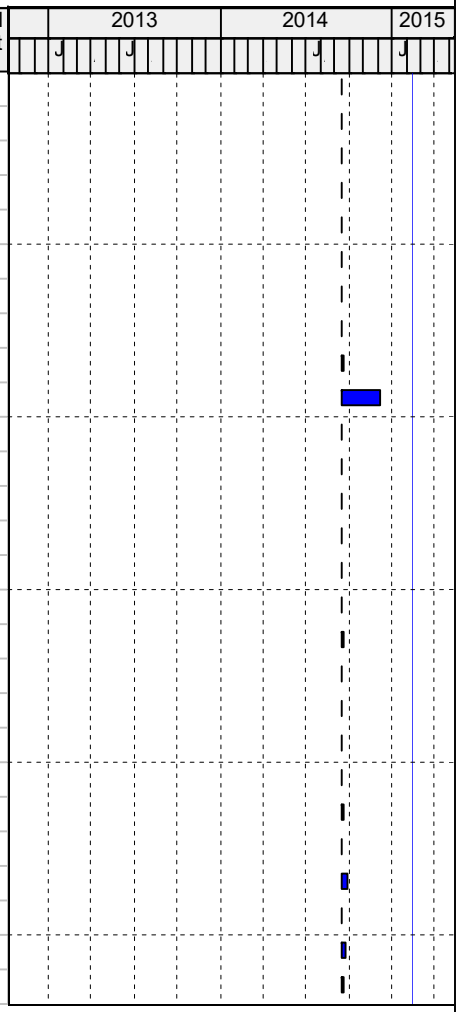



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7028 | GWB Hang/Tape/Finish | 5 | 0 | 18-Sep-14 A | 08-Dec-14 A | |
| LL4-6028 | LL4 - Frame Elevator Lobby | 2 | 0 | 18-Sep-14 A | 02-Oct-14 A | |
| MPT-1010a | Tower - Install E/W Wing, West End (Elev 52,53) | 8 | 0 | 18-Sep-14 A | 10-Oct-14 A | |
| LL2-2068 | LL2 - Generator Room - Electrical Finishes | 3 | 0 | 19-Sep-14 A | 30-Sep-14 A | |
| L07-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L09-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L04-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L05-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L03-8140 | Countertops On Site | 0 | 0 | 22-Sep-14 A | | |
| L03-8129a | Shower Doors On Site | 0 | 0 | 22-Sep-14 A | | |
| LL1-Z3-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L1BOH2-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2-2048a | LL2 - Move in Laundry Room Ironer | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2E-8122 | LL2 - Hang GWB at Fire Pump Room | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-FCC20 | FCC - Rough-In and Install Panels | 25 | 0 | 22-Sep-14 A | 21-Nov-14 A | |
| I-3014 | Core drill for MEP relocations | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L05-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L07-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 05-Dec-14 A | |
| L09-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 05-Dec-14 A | |
| L14-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 08-Dec-14 A | |
| L04-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L05-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L06-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L07-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L04-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |

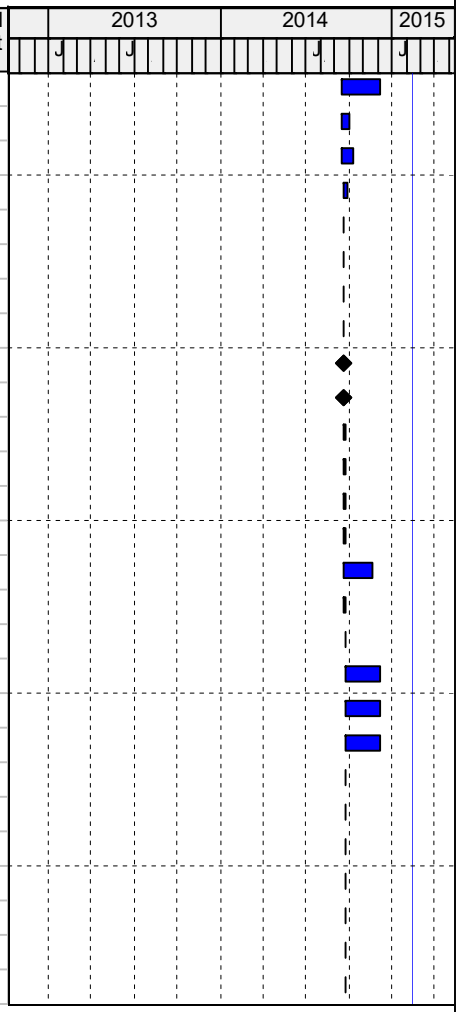



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L04-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L05-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-7122 | HVAC Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| LL2-2058 | LL2 - Tape/Finish Laundry Room | 3 | 0 | 24-Sep-14 A | 26-Sep-14 A | |
| L08-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L17-8395 | Framing at Elevator Lobby | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L05-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L06-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L07-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L08-7120 | Electrical Rough-In | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| LL2E-8124 | LL2 - Temp-In Louver Opening at Fire Pump Room | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L1-5104c | L1 - Install Storefront at Main Entry Facade | 5 | 0 | 25-Sep-14 A | 10-Oct-14 A | |
| L16-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L08-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L10-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L16-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L17-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L17-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |

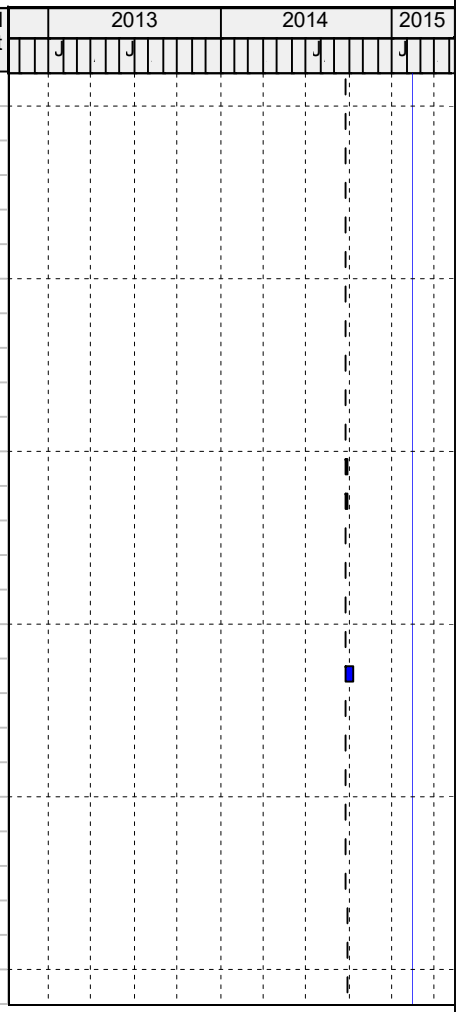



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L11-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L12-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L14-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L15-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L17-7118 | Install HM Door Frame | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| LL3-6030 | LL3 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL4-6030 | LL4 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL2-6034 | LL2 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L1BOH2-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L02-6030 | L2 - Framing at Elevator Lobby & North Half | 4 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| MPT-1022 | Tower - Caulking, west | 8 | 0 | 29-Sep-14 A | 03-Nov-14 A | |
| PH-6015 | PH - Set Boilers and Pumps | 12 | 0 | 29-Sep-14 A | 15-Oct-14 A | |
| L11-8204 | Bathrooms - Vinyl Wall Coverings | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L10-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L17-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L11-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L12-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L07-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 30-Sep-14 A | 08-Oct-14 A | |
| L11-8201 | Install ACT Grid @ Corridors | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L09-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L09-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L11-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |

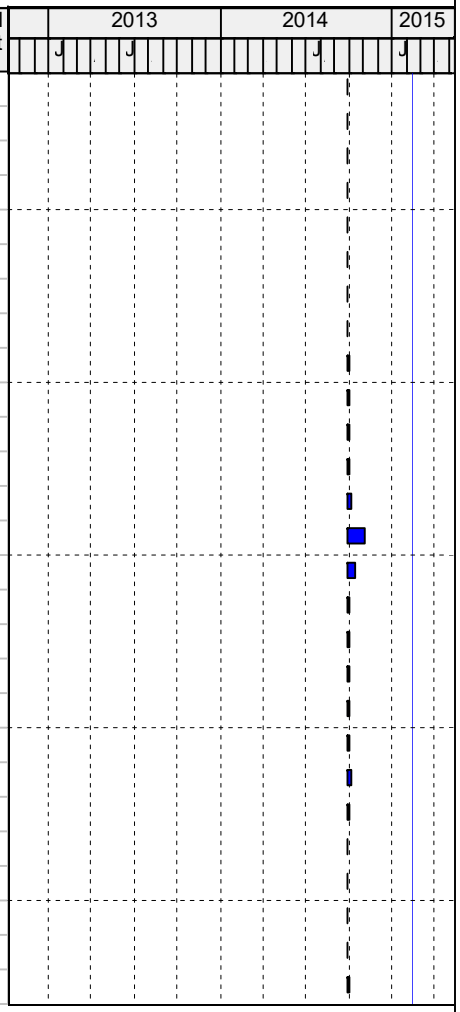



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L14-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L15-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| LL2-2072 | Generator - Complete generator and annunciator cor | 5 | 0 | 30-Sep-14 A | 21-Oct-14 A | |
| L17-6040 | Test Heat Pumps - L16 and L17 | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L17-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L14-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L03-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |

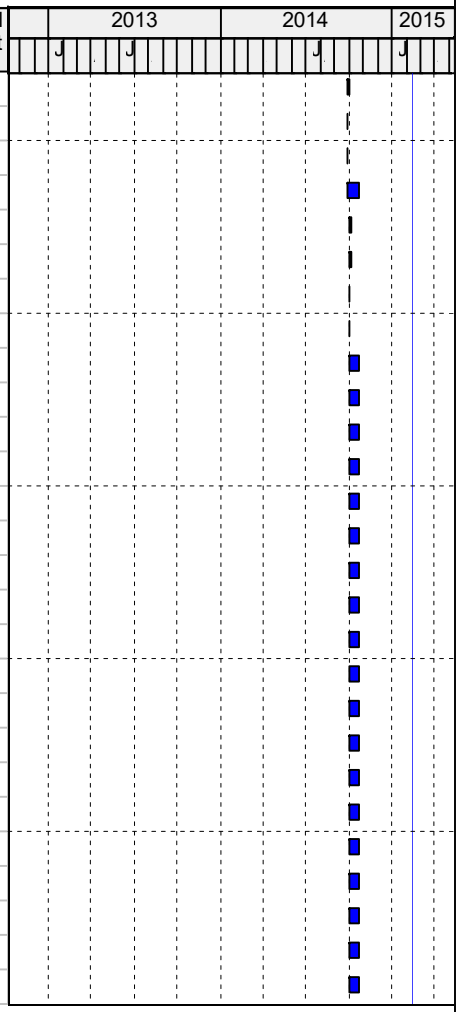



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L11-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L12-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L12-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L14-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L16-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L17-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L09-8136 | Install Counter Subtops | 3 | 0 | 01-Oct-14 A | 03-Oct-14 A | |
| L02-6032 | L2 - Electrical RI at Elevator Lobby & North Half | 5 | 0 | 01-Oct-14 A | 08-Oct-14 A | |

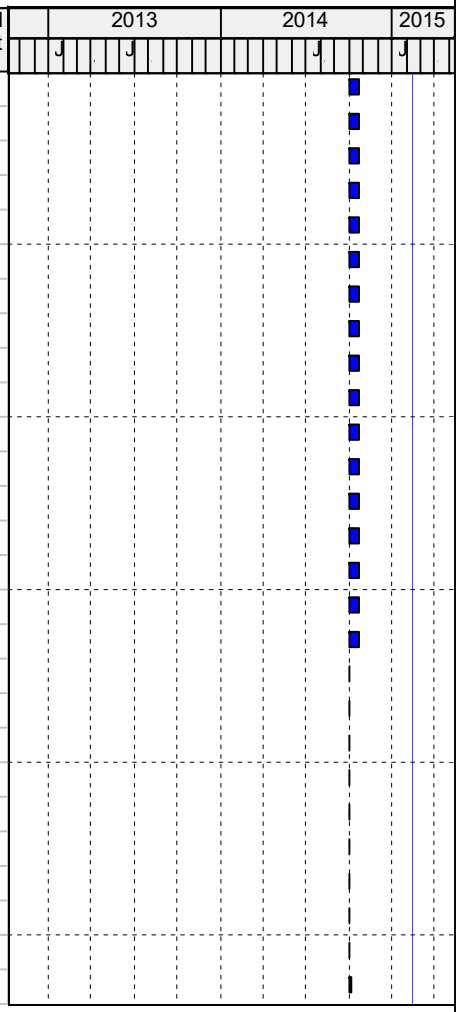



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2306 | Prep, grind and overlay at 11th Ave, 3rd Place & 2nd | 5 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 01-Oct-14 A | 16-Dec-14 A | |
| L16-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L14-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L15-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1BOH2-8130 | Inspections For Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L02-6024a | L2 - Inspections - South Half | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L06-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| L17-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| LL2-2074 | Generator - Install fuel fill | 2 | 0 | 03-Oct-14 A | 06-Oct-14 A | |
| L07-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| MPT-1020 | Tower - Install E/W Wing, East End (Elev 41,44) | 5 | 0 | 06-Oct-14 A | 18-Oct-14 A | |
| LL1-8102a | GWB Hang/Tape (Ceilings) | 10 | 0 | 06-Oct-14 A | 18-Nov-14 A | |
| L1BOH2C-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6014 | Complete Plumbing RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6016 | Complete Electrical RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6018 | Complete HVAC RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L03-8200a | New murals on site (date estimated) | 0 | 0 | 06-Oct-14 A | | |
| SW-2100 | Zone 1 - Survey curb & site lighting | 2 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 06-Oct-14 A | 06-Oct-14 A | |
| L1BOH2-8100 | Insulation | 4 | 0 | 07-Oct-14 A | 13-Oct-14 A | |

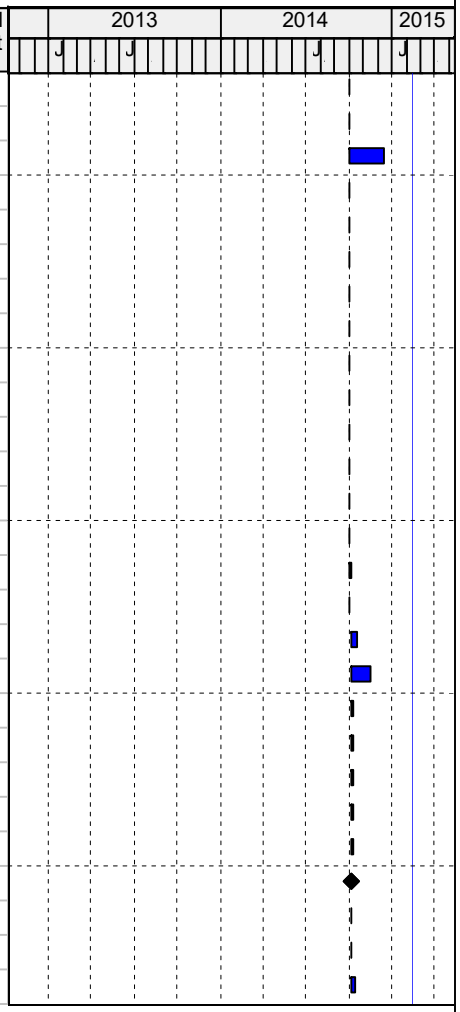


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L12-8201 | Install ACT Grid @ Corridors | 2 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| L10-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 07-Oct-14 A | 20-Oct-14 A | |
| L03-8216x | Vinyl Wall Coverings - Install Murals | 2 | 0 | 07-Oct-14 A | 29-Dec-14 A | |
| L1B-8102b | GWB Hang (Walls) & Inspection - Exterior Wall at Cor | 3 | 0 | 07-Oct-14 A | 09-Oct-14 A | |
| RF-4048 | Tower Roof - Install davit arms | 3 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| LL2-2076 | Generator - Install fuel fill mechanical piping | 4 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L12-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L09-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L03-8633 | Pool - Install waterproofing & test | 3 | 0 | 08-Oct-14 A | 17-Oct-14 A | |
| L03-8130 | Install Door Hardware | 3 | 0 | 08-Oct-14 A | 28-Oct-14 A | |
| L10-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L02-8102a | L2 - GWB Hang / Tape / Finish - South Half | 7 | 0 | 09-Oct-14 A | 27-Oct-14 A | |
| SW-2102 | Zone 1 - Vacate SE corner | 2 | 0 | 09-Oct-14 A | 11-Oct-14 A | |
| SW-2106 | Zone 1 - Sawcut and remove asphalt | 4 | 0 | 09-Oct-14 A | 14-Oct-14 A | |
| L11-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 09-Oct-14 A | |
| SW-2200 | Zone 2 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |
| SW-2300 | Zone 3 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |
| SW-2108 | Zone 1 - Install east footing drain | 4 | 0 | 10-Oct-14 A | 20-Oct-14 A | |
| L04-8130 | Install Door Hardware | 3 | 0 | 10-Oct-14 A | 29-Oct-14 A | |
| ML-5962 | Man/Material Lifts - Remove Roof Lift Stop | 0 | 0 | | 11-Oct-14 A | |
| I-1102 | Additional work at new L17 guest rooms | 5 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| LL2-2046 | LL2 - Generator Room - Misc. Finishes | 3 | 0 | 13-Oct-14 A | 21-Nov-14 A | |
| RF-4008 | Tower Roof - Install corrugated metal panels | 5 | 0 | 13-Oct-14 A | 03-Nov-14 A | |
| MPT-1018b | Tower - Roof cornice frame & sheath | 6 | 0 | 13-Oct-14 A | 24-Oct-14 A | |
| L02-8100a | L2 - Insulation - South Half | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| SW-2112 | Zone 1 - Grade for curb and gutter | 3 | 0 | 13-Oct-14 A | 17-Oct-14 A | |

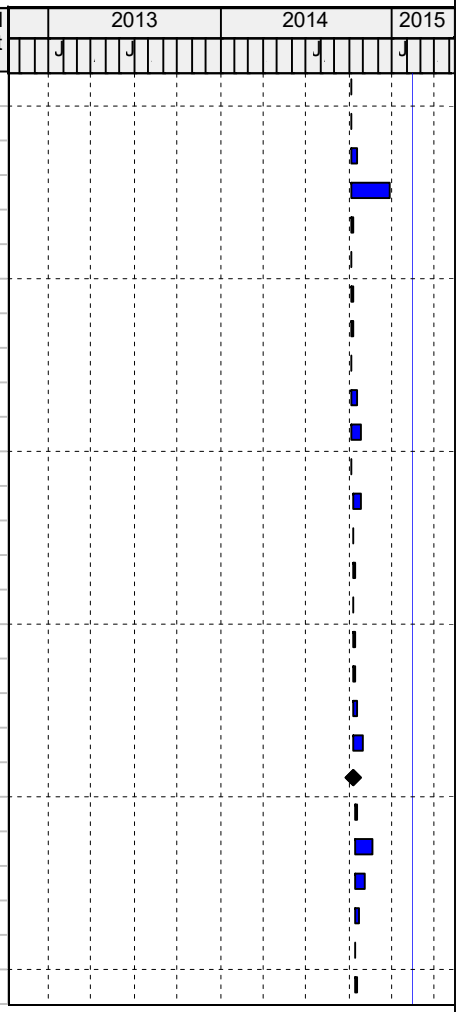



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2202 | Zone 2 - Install site lighting | 5 | 0 | 13-Oct-14 A | 24-Nov-14 A | |
| SW-2204 | Zone 2 - Repave utility trenches | 4 | 0 | 13-Oct-14 A | 22-Oct-14 A | |
| L12-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 13-Oct-14 A | |
| SW-2302 | Zone 3 - Grade for curb and gutter | 2 | 0 | 14-Oct-14 A | 01-Dec-14 A | |
| L14-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 14-Oct-14 A | 16-Oct-14 A | |
| L05-8130 | Install Door Hardware | 3 | 0 | 14-Oct-14 A | 03-Nov-14 A | |
| L14-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 14-Oct-14 A | |
| L16-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L15-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 15-Oct-14 A | 17-Oct-14 A | |
| L15-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 15-Oct-14 A | |
| SW-2206 | Zone 2 - Grade for curb and gutter | 2 | 0 | 16-Oct-14 A | 20-Oct-14 A | |
| MPP-1000 | Podium - Install W/S/N Elevations (Elev 1-5, 6,9-19,2 | 10 | 0 | 20-Oct-14 A | 10-Dec-14 A | |
| L06-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 20-Oct-14 A | 23-Oct-14 A | |
| LL2-8106a | LL2, Garage - Pinned Insulation (except at ramp) | 4 | 0 | 20-Oct-14 A | 04-Dec-14 A | |
| L1B-8102d | GWB Hang (Walls) & Inspection - Main Ballroom East | 1 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| SW-2114 | Zone 1 - FRP curb and gutter | 2 | 0 | 20-Oct-14 A | 14-Nov-14 A | |
| RF-4044 | Ballroom Roof - Install metal coping | 3 | 0 | 20-Oct-14 A | 13-Nov-14 A | |
| L08-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 21-Oct-14 A | 23-Oct-14 A | |
| MPT-1018 | Tower - Install Roof Penthouse (Elev 36b,37,38.39) | 5 | 0 | 21-Oct-14 A | 05-Dec-14 A | |
| L11-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2208 | Zone 2 - FRP curb and gutter | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2304 | Zone 3 - FRP curb and gutter | 3 | 0 | 21-Oct-14 A | 02-Dec-14 A | |

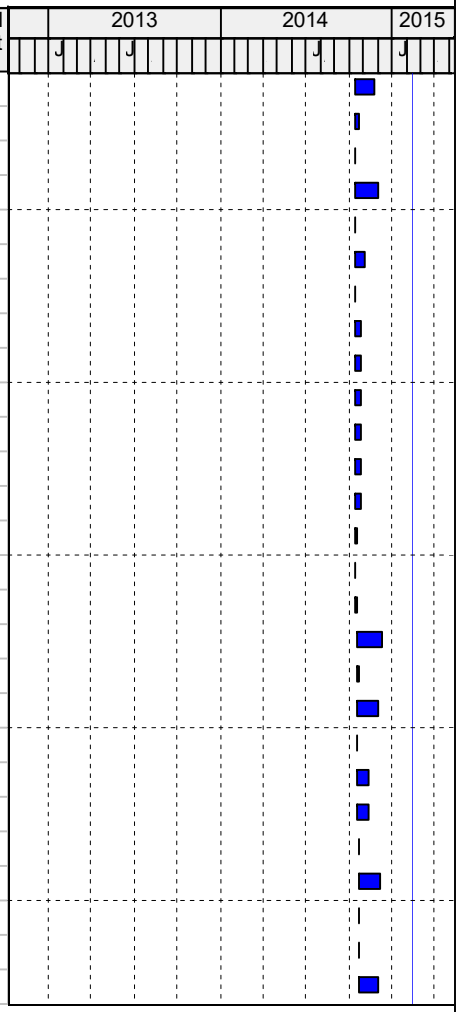



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L06-8130 | Install Door Hardware | 3 | 0 | 21-Oct-14 A | 03-Nov-14 A | |
| I-5100 | Resolve changes (ASI's and RFI's) | 1 | 0 | 21-Oct-14 A | 07-Jan-15 A | |
| L03-8634 | Pool - Install reinforcing steel & inspect | 5 | 0 | 22-Oct-14 A | 30-Oct-14 A | |
| MPT-1016 | Tower - Install N/S Wing, S. End W. of Manlift (Elev 2 | 5 | 0 | 22-Oct-14 A | 05-Dec-14 A | |
| SW-2116 | Zone 1 - Fine grade for sidewalk | 3 | 1 | 22-Oct-14 A | 04-Mar-15 | 27 |
| LL4-8106 | LL4 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| LL3-8106 | LL3 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L14-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L08-8130 | Install Door Hardware | 3 | 0 | 22-Oct-14 A | 04-Nov-14 A | |
| L07-8130 | Install Door Hardware | 3 | 0 | 22-Oct-14 A | 03-Nov-14 A | |
| L03-8606 | L3 Pool - HVAC R/I | 3 | 0 | 23-Oct-14 A | 27-Oct-14 A | |
| L09-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 23-Oct-14 A | 03-Nov-14 A | |
| L12-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| LL2-2078 | Generator - Install fuel fill control wiring | 2 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| RF-4050 | Roof at Manlift - Erect steel | 1 | 0 | 24-Oct-14 A | 24-Oct-14 A | |
| CO-7204 | Cx - Gas Service established | 0 | 0 | | 24-Oct-14 A | |
| I-5900 | Owner select color for Porte Cochere drive concrete | 20 | 5 | 24-Oct-14 A | 20-Feb-15 | 28 |
| L1BOH2-8102 | GWB Hang (Walls) | 4 | 0 | 27-Oct-14 A | 07-Nov-14 A | |
| L04-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 27-Oct-14 A | 12-Nov-14 A | |
| RF-4052 | Roof at Manlift - Framing/sheathing/air barrier (inspec | 4 | 0 | 27-Oct-14 A | 30-Oct-14 A | |
| LL2-2080 | Generator - Complete generator accessories (battery) | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| LL2-2082 | Generator - Cx fuel fill | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| L09-8130 | Install Door Hardware | 3 | 0 | 28-Oct-14 A | 04-Nov-14 A | |
| CO-7158 | Generator - Interim electrical inspection | 1 | 0 | 29-Oct-14 A | 29-Oct-14 A | |
| LL2-2070 | LL2 - Generator Room - Generator Ready for Startup | 0 | 0 | | 30-Oct-14 A | |
| LL2-2084 | Generator - Initial fuel fill | 1 | 0 | 30-Oct-14 A | 30-Oct-14 A | |

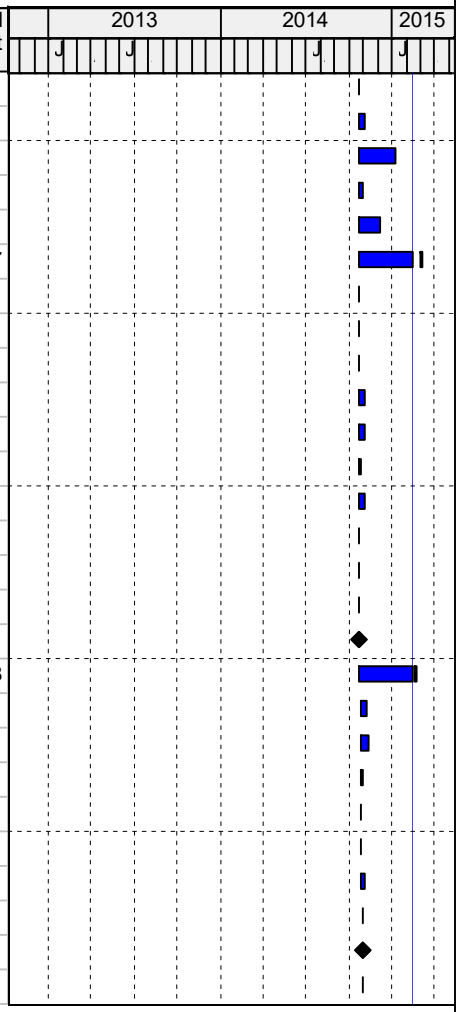


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7200 | Cx - Penthouse Mechanical Installation Complete | 0 | 0 | | 30-Oct-14 A | |
| EL-6028 | Elev 6 - RFI-761: Response, pricing, complete work (r | 20 | 0 | 30-Oct-14 A | 27-Jan-15 A | |
| L03-8636 | Pool - Shotcrete | 1 | 0 | 31-Oct-14 A | 31-Oct-14 A | |
| RF-4054 | Roof at Manlift - Final mechanical installations | 4 | 0 | 31-Oct-14 A | 05-Nov-14 A | |
| RF-4056 | Roof at Manlift - Final electrical connections | 2 | 0 | 31-Oct-14 A | 05-Nov-14 A | |
| CO-7130 | Fire Alarm - Point-To-Point Wiring | 18 | 0 | 01-Nov-14 A | 06-Feb-15 A | |
| L03-8404 | GWB Hang/Tape Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 14-Nov-14 A | |
| L04-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 14-Nov-14 A | |
| L05-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 17-Nov-14 A | |
| L06-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 17-Nov-14 A | |
| L03-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L04-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L05-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L06-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L07-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L08-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L09-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L10-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L11-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L12-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L14-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L15-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L16-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L17-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L14-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 03-Nov-14 A | 06-Nov-14 A | |
| MPT-1024 | (A) Caulking - Elevation 41 (east elevation above poo | 7 | 0 | 03-Nov-14 A | 16-Dec-14 A | |
| CO-7206 | Cx - Purge/Prove Gas-Fed Equipment and Feeder Li | 7 | 0 | 03-Nov-14 A | 09-Nov-14 A | |

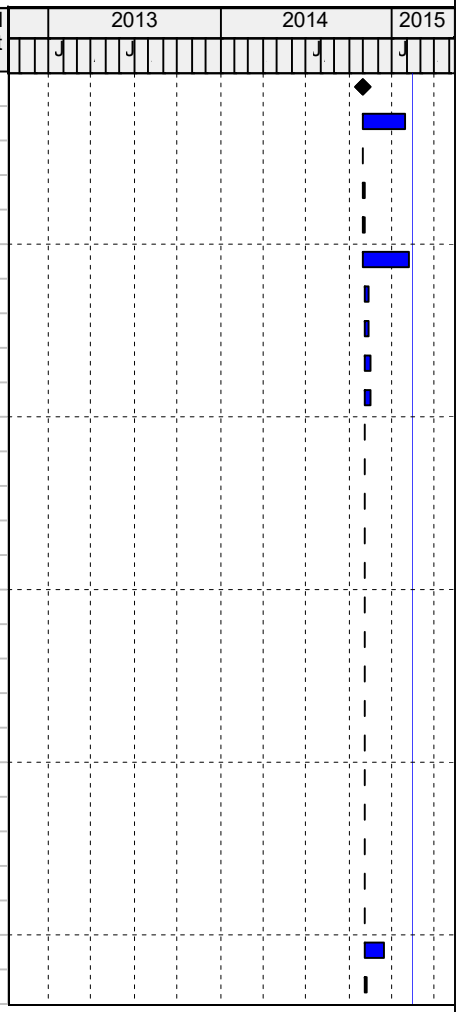



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 17-Nov-14 A | |
| L08-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L09-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L10-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L12-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L11-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 04-Nov-14 A | 15-Dec-14 A | |
| L11-8130 | Install Door Hardware | 3 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L10-8130 | Install Door Hardware | 3 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L11-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 18-Nov-14 A | |
| L12-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 19-Nov-14 A | |
| L14-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 19-Nov-14 A | |
| MPP-1010 | Podium - Install East Elevation (Elev 5 & 7) | 7 | 0 | 05-Nov-14 A | 10-Dec-14 A | |
| CO-7162 | Generator - Load bank testing | 1 | 0 | 05-Nov-14 A | 05-Nov-14 A | |
| CO-7202 | Cx - Electrical Internal Bus & LL2-L17 Bus Duct Energ | 0 | 0 | | 05-Nov-14 A | |
| CO-7202a | Cx - Energize normal power distribution | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| L15-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 19-Nov-14 A | |
| L16-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 20-Nov-14 A | |
| L17-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 20-Nov-14 A | |
| RF-4058 | Roof at Manlift - Install roofing | 2 | 0 | 06-Nov-14 A | 07-Nov-14 A | |
| CO-7164 | Generator - Final electrical inspection | 1 | 0 | 06-Nov-14 A | 06-Nov-14 A | |
| L15-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 07-Nov-14 A | 12-Nov-14 A | |
| L03-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L03-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L04-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L04-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L05-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L05-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |

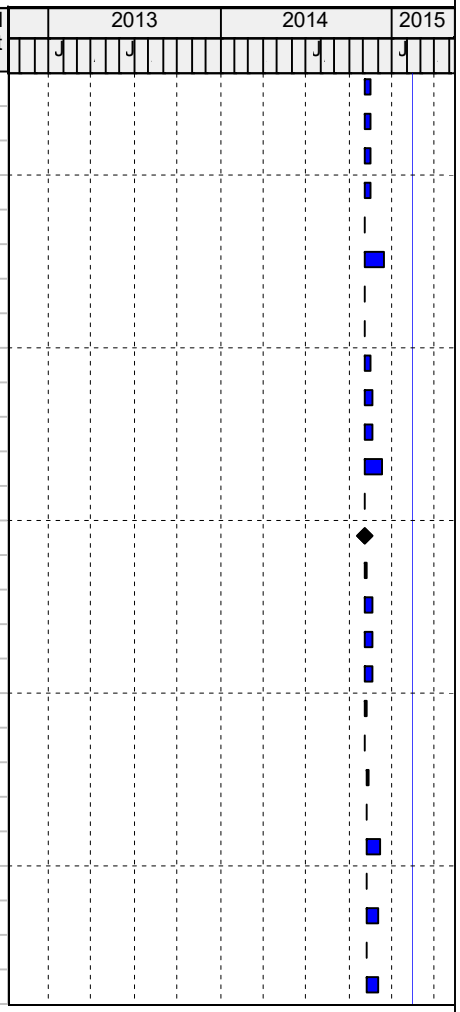



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L06-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L07-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L07-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L08-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L08-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L09-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L09-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L10-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L10-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L11-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L11-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L12-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L12-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L14-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L14-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L15-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L15-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L16-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L16-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L17-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L17-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L05-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| L06-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 10-Nov-14 A | 11-Nov-14 A | |
| MPT-1032 | Tower - Install sign backing NW (Elev 51,52) | 4 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L12-8130 | Install Door Hardware | 3 | 0 | 10-Nov-14 A | 12-Nov-14 A | |
| EL-1230 | Elev 1&2 - Complete hoistway ventilation | 13 | 0 | 10-Nov-14 A | 15-Dec-14 A | |

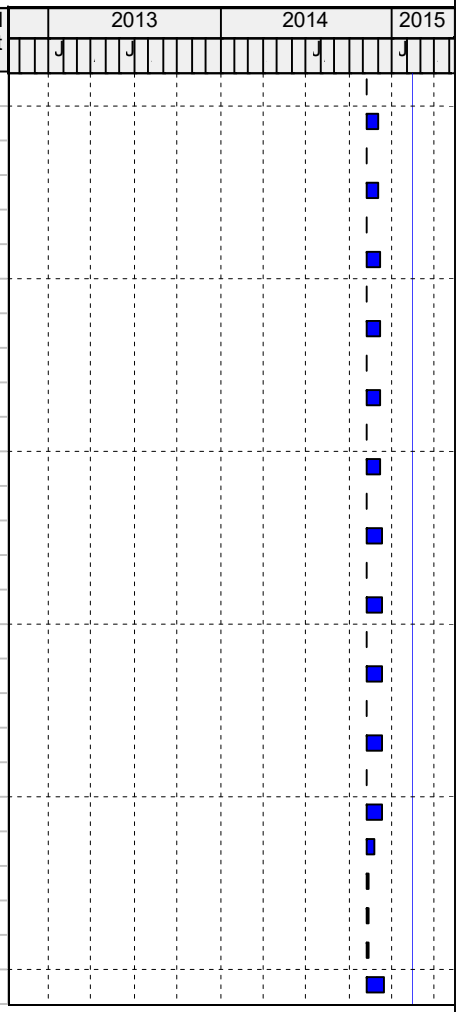



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-1232 | Elev 1&2 - Wire & startup AC split units | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-1234 | Elev 1&2 - Install EMR doors, hardware & labeling | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-3428 | Elev 3&4 - Complete hoistway ventilation | 13 | 0 | 10-Nov-14 A | 15-Dec-14 A | |
| EL-3430 | Elev 3&4 - Wire & startup AC split units | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-3432 | Elev 3&4 - Install EMR doors, hardware & labeling | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-6030 | Elev 6 - Complete fire-rated assemblies at hoistway, l | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| L07-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 11-Nov-14 A | 12-Nov-14 A | |
| L16-8106 | Paint - Accent Walls | 2 | 0 | 11-Nov-14 A | 12-Nov-14 A | |
| L14-8130 | Install Door Hardware | 3 | 0 | 11-Nov-14 A | 13-Nov-14 A | |
| L03-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 12-Nov-14 A | 18-Nov-14 A | |
| SW-2104 | Zone 1 - Install lighting conduit at SE corner | 2 | 0 | 12-Nov-14 A | 14-Nov-14 A | |
| L16-8111 | Paint - Door Jambs | 2 | 0 | 12-Nov-14 A | 13-Nov-14 A | |
| EL-6010i | Elev 6 - Pit Slab Correction (form/pour/strip/clean) | 10 | 0 | 12-Nov-14 A | 26-Nov-14 A | |
| SW-2024 | Zone 4 - FRP Porte Cochere planter & bench | 6 | 0 | 12-Nov-14 A | 04-Dec-14 A | |
| L08-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| SW-2109 | Zone 1 - Install irrigation sleeves | 2 | 0 | 13-Nov-14 A | 14-Nov-14 A | |
| MPT-1026 | (C) Caulking - Elevation 47 (north elevation, east half | 10 | 0 | 13-Nov-14 A | 19-Dec-14 A | |
| L16-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| L15-8130 | Install Door Hardware | 3 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| L04-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 14-Nov-14 A | 19-Nov-14 A | |
| SW-2203 | Zone 2 - Install irrigation sleeves | 2 | 0 | 14-Nov-14 A | 08-Jan-15 A | |
| L1B-8120 | Install operable partitions | 3 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| LL1-Z3-8340 | Install walk-in cooler/freezer (BY OTHERS) | 5 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| SW-2316 | Zone 3 - Demolish manlift shack and base | 5 | 0 | 17-Nov-14 A | 20-Nov-14 A | |
| I-1610 | Enclosure at manlift - Install exterior wall panels & ins | 5 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| L04-8140 | Install window sills | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| L03-8140x | Install window sills | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |

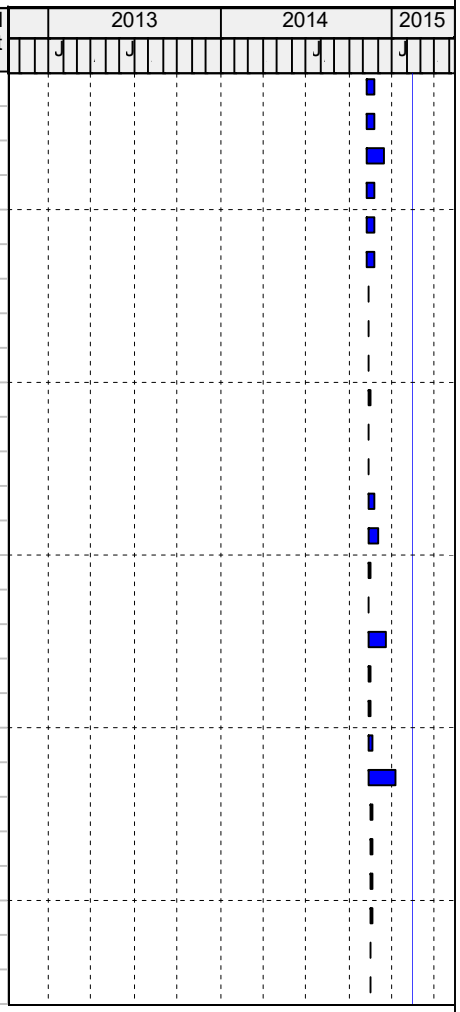



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| SW-2014 | Porte Cochere - Electrical rough-in | 5 | 0 | 17-Nov-14 A | 08-Dec-14 A | |
| I-5600 | Lower heat pump and install access panels (RFI 734) | 13 | 0 | 17-Nov-14 A | 09-Jan-15 A | |
| LL1-Z3-FCC26 | Program FACP & Stand-Up System | 20 | 0 | 17-Nov-14 A | 22-Jan-15 A | |
| L06-8140 | Install window sills | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L05-8140 | Install window sills | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L05-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 19-Nov-14 A | 22-Dec-14 A | |
| L16-8130 | Install Door Hardware | 3 | 0 | 19-Nov-14 A | 02-Dec-14 A | |
| L08-8140 | Install window sills | 2 | 0 | 19-Nov-14 A | 19-Nov-14 A | |
| L07-8140 | Install window sills | 2 | 0 | 19-Nov-14 A | 19-Nov-14 A | |
| I-1616 | Enclosure at manlift - Patch/repair concrete shear wal | 3 | 0 | 19-Nov-14 A | 21-Nov-14 A | |
| L10-8140 | Install window sills | 2 | 0 | 20-Nov-14 A | 20-Nov-14 A | |
| L09-8140 | Install window sills | 2 | 0 | 20-Nov-14 A | 20-Nov-14 A | |
| I-1622 | Manlift finishes - Install windows & caulk | 4 | 0 | 20-Nov-14 A | 03-Dec-14 A | |
| LL2-2060 | LL2 - Paint Laundry Room | 3 | 0 | 21-Nov-14 A | 24-Nov-14 A | |
| L03-8616 | L3 Pool - GWB above ceiling | 2 | 0 | 21-Nov-14 A | 22-Nov-14 A | |
| LL1-Z3-8342 | Final connections at walk-in cooler/freezer | 2 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L1K-8340 | Install walk-in cooler/freezer (BY OTHERS) | 2 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L10-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| L16-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| SW-2110 | Zone 1 - Adjust utilities structures | 5 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| SW-2214 | Zone 2 - Adjust utilities structures | 2 | 0 | 24-Nov-14 A | 25-Nov-14 A | |
| MPT-1030 | Tower - Install sign backing NE (Elev 44) | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| SW-2012 | Porte Cochere - Install cornice[DELETED SEE REV M | 8 | 0 | 24-Nov-14 A | 05-Dec-14 A | |
| L03-8650 | L3 Pool - Build scaffold at pool pit | 2 | 0 | 24-Nov-14 A | 25-Nov-14 A | |
| EL-6032 | Elev 6 - Install pit ladder | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| EL-6034 | Elev 6 - Install pit jack & hoistway pistons; connect hy | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |

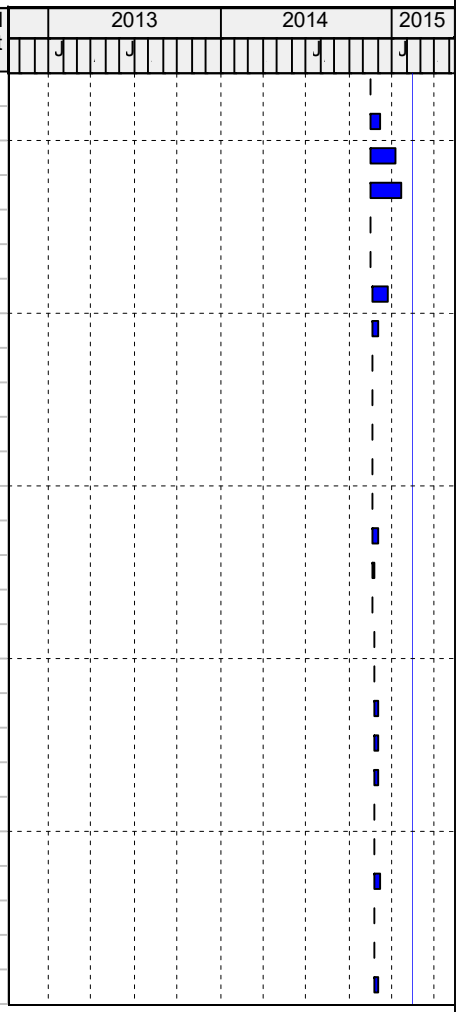



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 25-Nov-14 A | 22-Dec-14 A | |
| L02-8104a | L2 - Int Painting - South Half | 2 | 0 | 25-Nov-14 A | 26-Nov-14 A | |
| SW-2016 | Porte Cochere - Complete framing | 3 | 0 | 25-Nov-14 A | 01-Dec-14 A | |
| LL2-2096 | LL2 - Install FRP at Laundry Room | 8 | 0 | 25-Nov-14 A | 05-Dec-14 A | |
| I-1602 | Enclosure at manlift - Install shear wall clips and inspe | 4 | 0 | 26-Nov-14 A | 05-Dec-14 A | |
| L07-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| SW-2318 | Zone 3 - Install catch basin | 1 | 0 | 26-Nov-14 A | 26-Nov-14 A | |
| L03-8652 | L3 Pool - Frame ceiling | 4 | 0 | 26-Nov-14 A | 04-Dec-14 A | |
| L03-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L04-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L05-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L06-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L07-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L09-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L10-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L11-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L12-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L14-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L15-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L16-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L17-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 01-Dec-14 A | 04-Dec-14 A | |
| L02-6016a | L2 - Electrical Room Buildout | 5 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| L03-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L04-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L05-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |

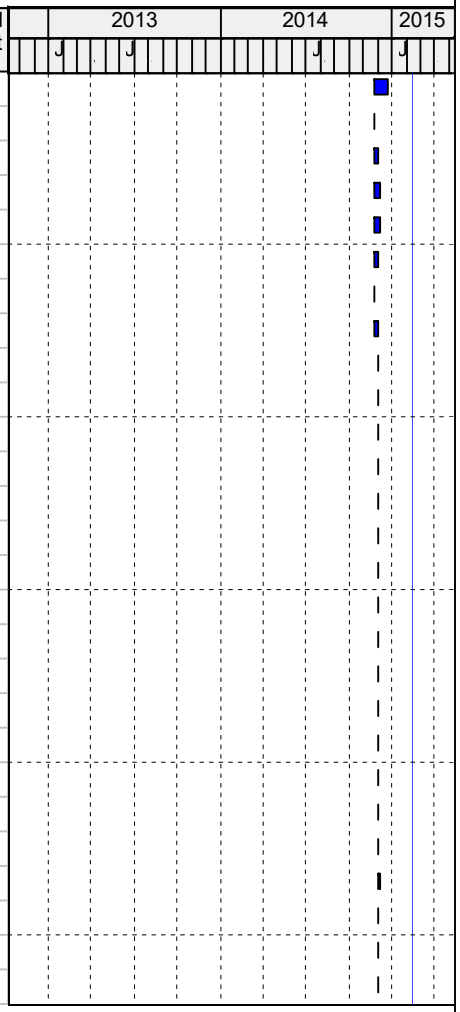



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L07-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L09-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L10-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L11-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L12-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L14-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L15-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L16-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L17-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| SW-2210 | Zone 2 - Fine grade for sidewalk | 5 | 0 | 01-Dec-14 A | 08-Jan-15 A | |
| RF-4040 | L2.5 Horseshoe - Install sheet metal capping[DELETI | 3 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| MPT-1042 | Enclosure at manlift - air barrier & inspect | 5 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| CO-7208 | Cx - Start-Up Pumps | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| CO-7210 | Cx - Start-Up VFD's | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| L17-8106 | Paint - Accent Walls | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| LL4-8116 | LL4 - Install ACT grid [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL3-8116 | LL3 - Install ACT grid [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| I-1630 | Manlift finishes - Framing, corridor ceilings & inspect | 4 | 0 | 01-Dec-14 A | 09-Dec-14 A | |
| EL-6036 | Elev 6 - Install shunt trip breaker | 5 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| L17-8111 | Paint - Door Jambs | 2 | 0 | 02-Dec-14 A | 03-Dec-14 A | |
| SW-2018 | Porte Cochere - GWB hang/tape | 3 | 0 | 02-Dec-14 A | 09-Dec-14 A | |
| L03-8654 | L3 Pool - HVAC drops at ceiling & inspect | 3 | 0 | 02-Dec-14 A | 05-Dec-14 A | |
| L11-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 03-Dec-14 A | 08-Dec-14 A | |
| SW-2308 | Zone 3 - Install site lighting | 5 | 0 | 03-Dec-14 A | 04-Dec-14 A | |
| L10-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 03-Dec-14 A | 15-Dec-14 A | |

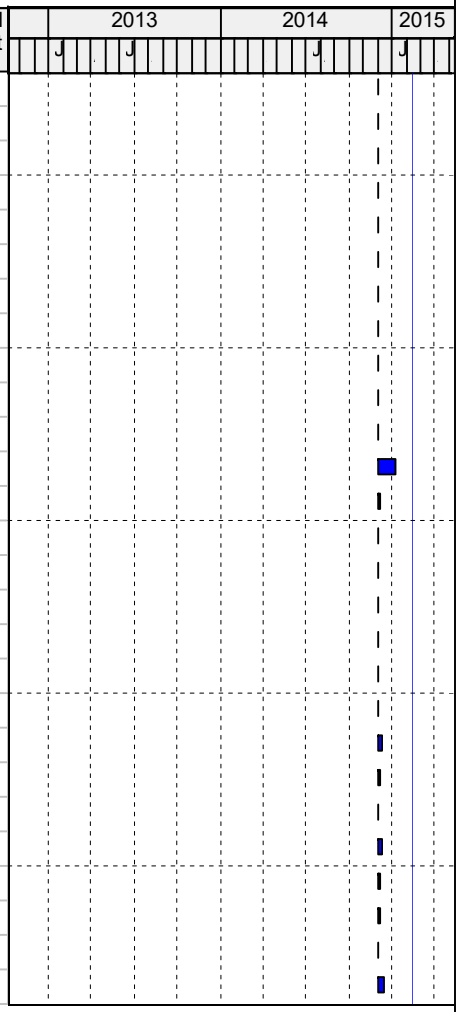



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1632 | Manlift finishes - Electrical rough-in & inspect | 2 | 0 | 03-Dec-14 A | 10-Dec-14 A | |
| SW-2028 | Zone 4 - Scan Porte Cochere deck | 2 | 0 | 04-Dec-14 A | 05-Dec-14 A | |
| I-1624 | Manlift finishes - Install batt insulation & inspect | 2 | 0 | 04-Dec-14 A | 04-Dec-14 A | |
| I-1626 | Manlift finishes - Shim window openings | 2 | 0 | 04-Dec-14 A | 05-Dec-14 A | |
| I-1628 | Manlift finishes - Install vapor barrier & inspect | 2 | 0 | 04-Dec-14 A | 08-Dec-14 A | |
| I-1608 | Tower - Install N/S Wing, S. End at manlift (Elev 32) [I | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1012 | Tower - Install N/S Wing, S. End E. Side Concrete (El | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| PC-4012 | Porte Cochere - Install sheet metal capping[DELETEI | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4046 | Tower Roof - Install sheet metal capping[DELETED S | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4060 | Roof at Manlift - Install corrugated metal panels[DELE | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4062 | Roof at Manlift - Install sheet metal capping[DELETEI | 2 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4064 | Pool Green Roof - Install sheet metal capping[DELET | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1040 | Tower - Install N/S Wing, S, End (Elev 30)[DELETED : | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1044 | Enclosure at manlift - Install sign backing south[DELE | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1612 | Enclosure at manlift - Caulking[DELETED SEE REV M | 8 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1614 | Enclosure at manlift - Install rigid insulation at shear w | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1618 | Enclosure at manlift - Install framing at shear wall[DEI | 5 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1620 | Enclosure at manlift - Install hat channel over framing | 5 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| L03-8656 | L3 Pool - Electrical rough-in at ceiling & inspect | 3 | 0 | 05-Dec-14 A | 19-Dec-14 A | |
| L1K-8344 | Set kitchen hoods | 8 | 0 | 06-Dec-14 A | 15-Dec-14 A | |
| L12-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L03-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |
| L04-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |
| L05-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |
| SW-2312 | Zone 3 - Fine grade for sidewalk | 3 | 0 | 08-Dec-14 A | 08-Jan-15 A | |
| RF-4042 | Pool Roof - Install metal coping at high roof | 2 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L17-8130 | Install Door Hardware | 3 | 0 | 08-Dec-14 A | 11-Dec-14 A | |

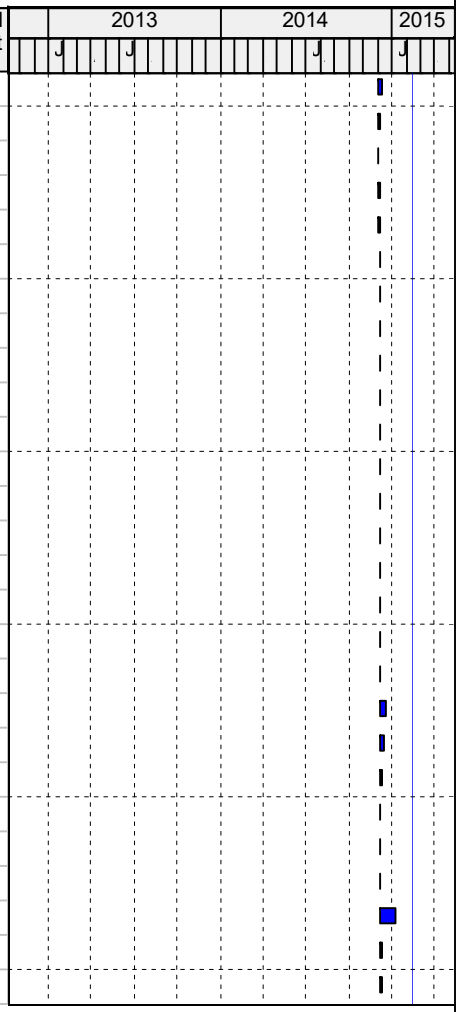



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L03-8658 | L3 Pool - Fire sprinkler drops at ceiling & inspect | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| LL2-8140 | LL2 - Install vinyl wall coverings | 2 | 0 | 08-Dec-14 A | 24-Dec-14 A | |
| L04-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L05-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L07-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L08-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L14-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L15-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 09-Dec-14 A | 12-Dec-14 A | |
| L03-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L07-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L08-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L04-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L05-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L07-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L08-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| RF-4072 | Pool Roof - Install metal coping | 3 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L17-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 09-Dec-14 A | 12-Dec-14 A | |
| L07-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 09-Dec-14 A | 29-Dec-14 A | |

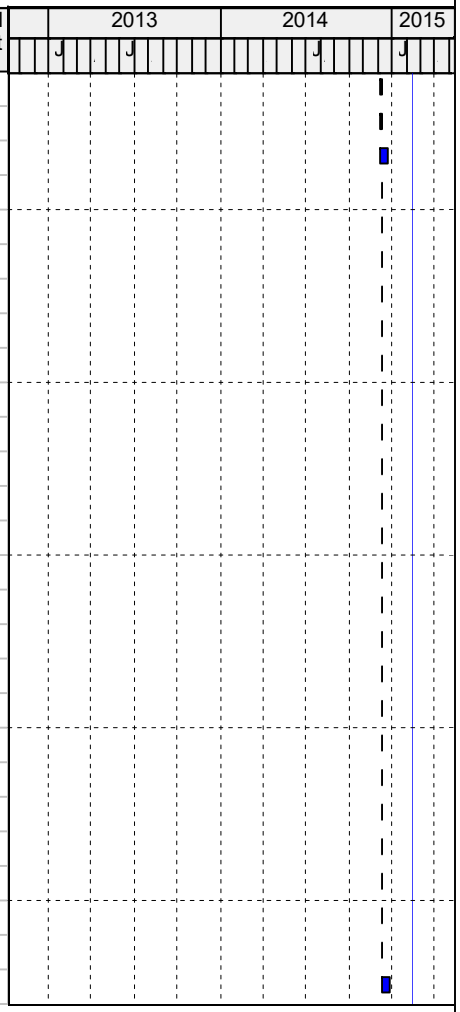



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 09-Dec-14 A | 24-Dec-14 A | |
| I-1604 | Manlift finishes - GWB, hang walls | 2 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L07-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L08-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 16-Dec-14 A | |
| L11-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L12-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L14-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L15-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L16-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L17-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| LL2E-8340 | LL2 - Install walk-in cooler/freezer (BY OTHERS) | 5 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L10-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 10-Dec-14 A | 17-Dec-14 A | |
| L09-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L10-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L11-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L11-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L12-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L14-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L15-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L16-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L17-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L08-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 10-Dec-14 A | 29-Dec-14 A | |
| I-1634 | Manlift finishes - GWB, hang ceilings | 2 | 0 | 10-Dec-14 A | 16-Dec-14 A | |
| L12-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L14-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L15-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L03-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 11-Dec-14 A | 11-Dec-14 A | |

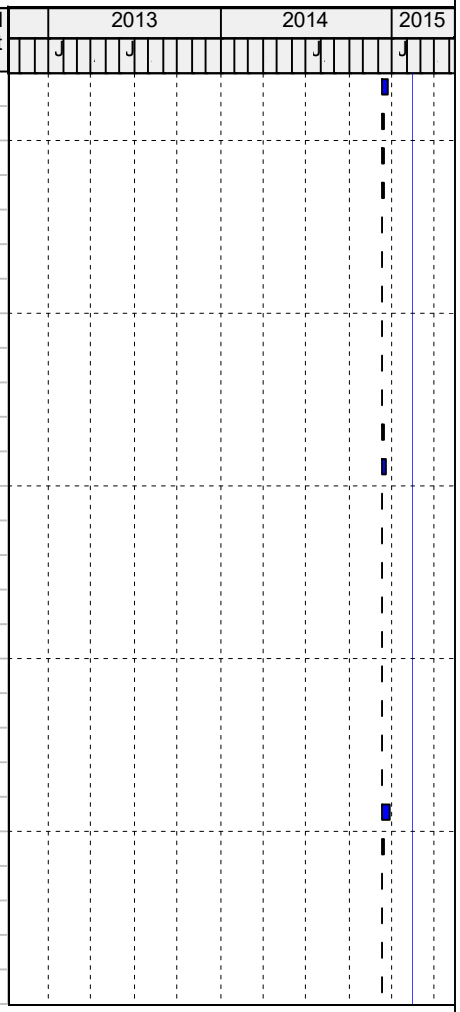



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| MPT-1034 | (A) Elevation 52 (west elevation, north end, L3-L18) | 4 | 0 | 11-Dec-14 A | 16-Dec-14 A | |
| MPT-1036 | (B) Elevation 45/46 (north elevation, east end, L3-L1 | 5 | 0 | 11-Dec-14 A | 19-Dec-14 A | |
| L16-7030 | Paint | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L17-7030 | Paint | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L05-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L06-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| MPT-1066 | Tower Sign, East (El. 32) - Install backing | 3 | 0 | 12-Dec-14 A | 22-Dec-14 A | |
| MPT-1076 | (B) Caulking - Elevation 51 (north elevation, west half | 10 | 0 | 12-Dec-14 A | 19-Dec-14 A | |
| L04-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L04-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L07-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L08-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L09-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L14-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L15-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L17-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 16-Dec-14 A | |
| L04-7042 | Install Tile Flooring (x41) | 2 | 0 | 15-Dec-14 A | 24-Dec-14 A | |
| L05-7042 | Install Tile Flooring (x41) | 2 | 0 | 15-Dec-14 A | 24-Dec-14 A | |
| LL4-8102a | LL4 - GWB Tape/Finish | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| LL3-8102a | LL3 - GWB Tape/Finish | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| L03-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L04-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |

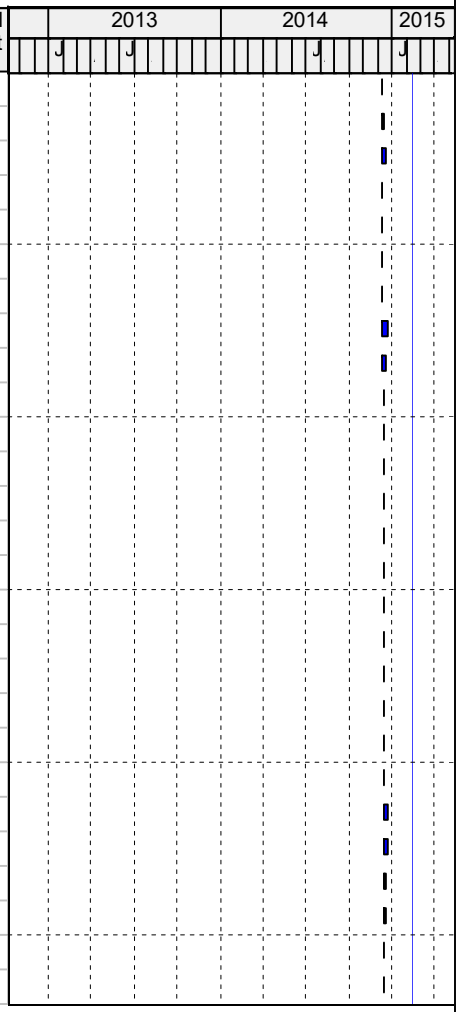



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L07-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L08-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L09-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L10-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| CO-7126 | Fire pump test pre-planning complete (see checklist) | 0 | 0 | | 15-Dec-14 A | |
| LL1-Z3-6034 | COB Correction - Add ceiling access panels in Food F | 10 | 0 | 15-Dec-14 A | 26-Jan-15 A | |
| I-5200 | Receive ceiling grid layout from owner and adjust ME | 8 | 1 | 15-Dec-14 A | 16-Feb-15 | 7 |
| L03-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| L05-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L09-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L10-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L10-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L11-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L11-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L14-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L15-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L16-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L17-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| LL2E-8342 | LL2 - Final connections at walk-in cooler/freezer | 5 | 0 | 16-Dec-14 A | 05-Jan-15 A | |
| L11-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 16-Dec-14 A | 18-Dec-14 A | |
| L16-8201 | Corridors - Install ACT Grid | 2 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L06-7042 | Install Tile Flooring (x41) | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L07-7042 | Install Tile Flooring (x41) | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |

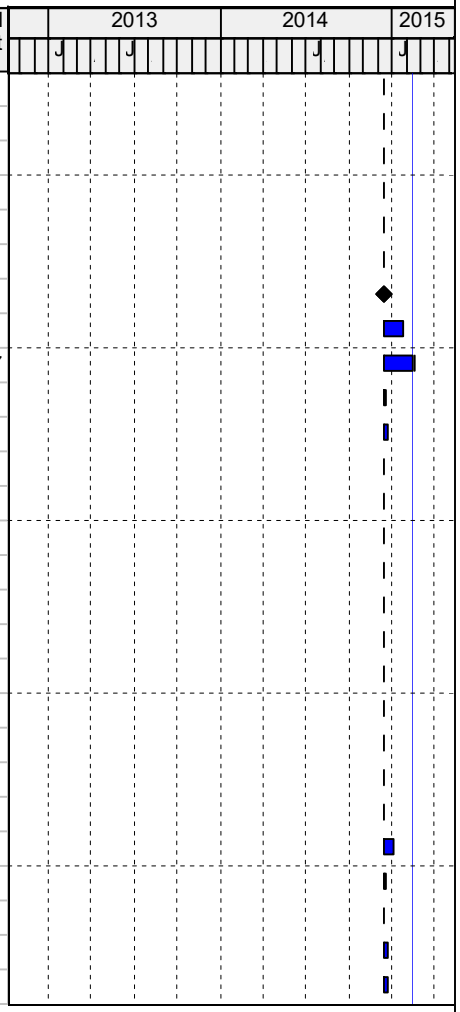



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-8102a | GWB Hang (Ceilings) & Inspection | 3 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L11-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L14-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L15-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L16-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L17-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| CO-7128 | Run fire pump test | 2 | 0 | 16-Dec-14 A | 17-Dec-14 A | |
| L09-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 16-Dec-14 A | 30-Dec-14 A | |
| SW-2026 | Zone 4 - FRP NW planter | 5 | 0 | 16-Dec-14 A | 05-Jan-15 A | |
| I-5370 | (S) Resolve south tower sign backing (RFI 844) | 5 | 0 | 16-Dec-14 A | 09-Jan-15 A | |
| L03-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 22-Dec-14 A | |
| L04-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 23-Dec-14 A | |
| L06-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 29-Dec-14 A | |
| L07-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 30-Dec-14 A | |
| L08-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 31-Dec-14 A | |
| L09-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 05-Jan-15 A | |
| L14-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L15-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L16-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L17-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L08-7042 | Install Tile Flooring (x41) | 2 | 0 | 17-Dec-14 A | 24-Dec-14 A | |
| L09-7042 | Install Tile Flooring (x41) | 2 | 0 | 17-Dec-14 A | 24-Dec-14 A | |
| L04-7136 | Install Door and Hardware | 1 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L16-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 17-Dec-14 A | 29-Dec-14 A | |
| MPT-1046 | (A) Elevation 26/27/53 (west elevation, south of 52, L | 3 | 0 | 17-Dec-14 A | 18-Dec-14 A | |
| MPT-1057 | (S) Elevation 32 framing (south elevation, east of mai | 5 | 0 | 17-Dec-14 A | 19-Jan-15 A | |

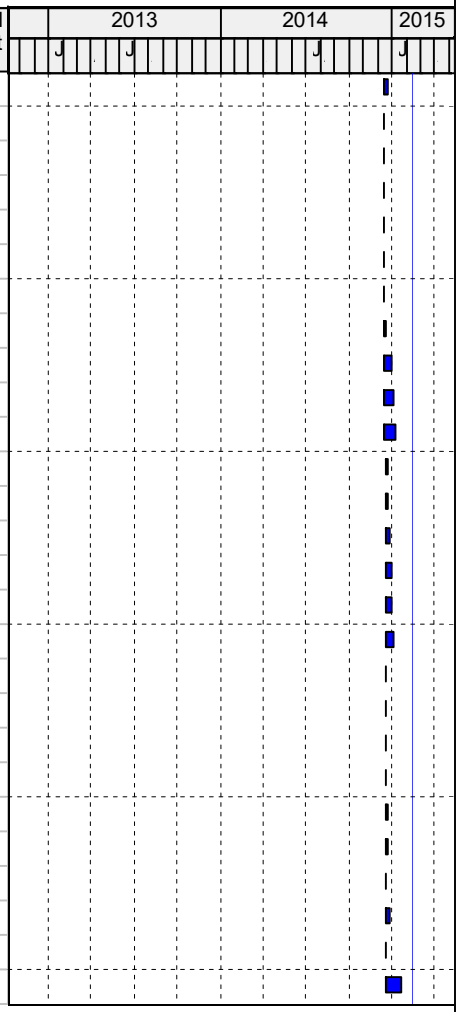



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPT-1080 | (A) Caulking - Elevation 44 (east elevation above poo | 8 | 0 | 17-Dec-14 A | 22-Dec-14 A | |
| LL1-Z2-8108 | Framing, ceiling clouds (incl. inspection) | 5 | 0 | 17-Dec-14 A | 22-Jan-15 A | |
| MPP-1006 | (C) Install Level 3 cornice metal (north, west & south) | 6 | 0 | 18-Dec-14 A | 30-Jan-15 A | |
| L10-7042 | Install Tile Flooring (x41) | 2 | 0 | 18-Dec-14 A | 24-Dec-14 A | |
| L11-7042 | Install Tile Flooring (x41) | 2 | 0 | 18-Dec-14 A | 24-Dec-14 A | |
| L12-7042 | Install Tile Flooring (x41) | 2 | 0 | 19-Dec-14 A | 24-Dec-14 A | |
| L14-7042 | Install Tile Flooring (x41) | 2 | 0 | 19-Dec-14 A | 24-Dec-14 A | |
| MPT-1048 | (B) Elevation 37 (penthouse east) | 3 | 0 | 19-Dec-14 A | 20-Dec-14 A | |
| I-5000 | Resolve RFI's and site work changes (new drawings) | 10 | 5 | 19-Dec-14 A | 20-Feb-15 | 19 |
| I-5002 | Resolve RFI's and site work changes (new drawings) | 20 | 0 | 19-Dec-14 A | 09-Feb-15 A | |
| I-5003 | Resolve RFI's and site work changes (new drawings) | 10 | 5 | 19-Dec-14 A | 20-Feb-15 | 21 |
| I-5004 | Resolve RFI's and site work changes (new drawings) | 1 | 0 | 19-Dec-14 A | 16-Jan-15 A | |
| L03-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 22-Dec-14 A | 22-Dec-14 A | |
| L07-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L17-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| CO-7212 | Cx - Start-Up Boilers | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L17-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L08-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L07-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L06-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L05-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L04-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 22-Dec-14 A | |
| I-1636 | Manlift finishes - GWB, tape & finish | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| EL-6038 | Elev 6 - Rough-in call boxes & lanterns | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| EL-6052 | Elev 6 - Complete hoistway ventilation | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| MPT-1078 | (C) Caulking - Elevation 37/38/39 (penthouse) | 4 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| MPT-1086 | (A) Caulking - Elevation 45/46 (north elevation, east e | 7 | 0 | 22-Dec-14 A | 29-Dec-14 A | |

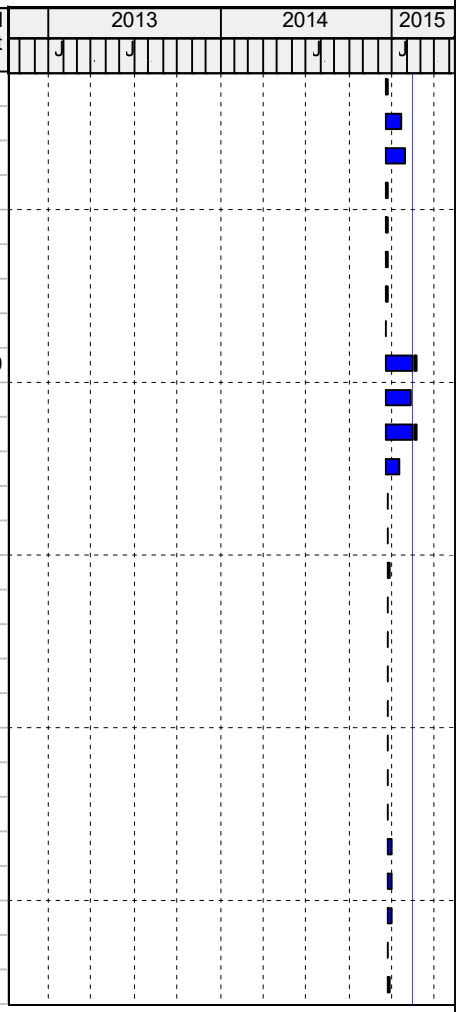



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPT-1088 | (B) Caulking - Elevation 52/53/26/27 (west elevation, | 11 | 0 | 22-Dec-14 A | 02-Jan-15 A | |
| MPP-1044 | Caulking - Elevation 9/10/11/12/13 (upper ballroom) | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| MPP-1046 | Caulking - Elevation 5/6 (east elevation, south end) | 8 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| L03-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L03-7032 | Install VCT Flooring (x42) | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L08-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L10-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L09-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L09-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 24-Dec-14 A | 29-Dec-14 A | |
| L03-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 31-Dec-14 A | |
| L15-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L16-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L17-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L04-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L05-7136 | Install Door and Hardware | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L10-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L17-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| LL1-Z3-8202 | Install FRP wall coverings | 4 | 0 | 29-Dec-14 A | 06-Jan-15 A | |
| L04-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L05-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L06-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L07-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L08-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L09-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L10-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL2-8130 | LL2 - Install ceiling grid | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| I-5300 | Heat Pump Revision - demo existing ceiling framing | 2 | 0 | 29-Dec-14 A | 29-Dec-14 A | |

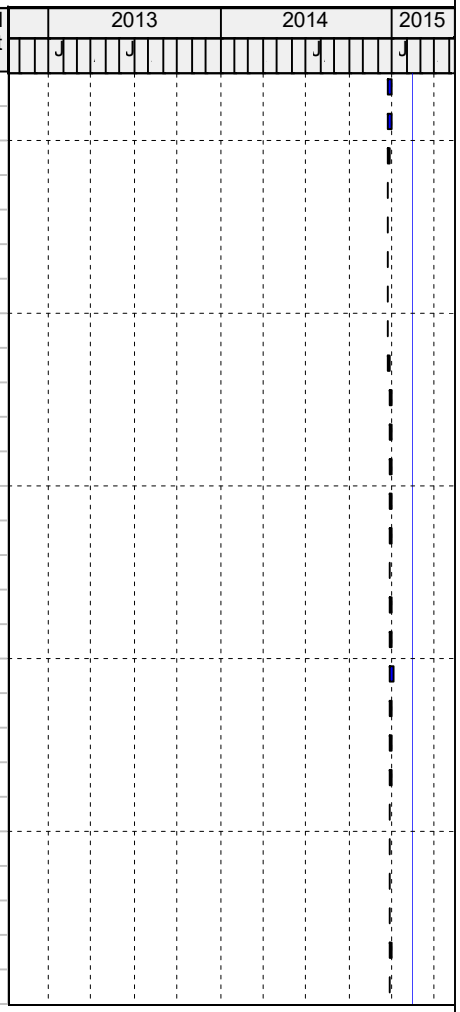



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 30-Dec-14 A | 05-Jan-15 A | |
| L06-7136 | Install Door and Hardware | 1 | 0 | 30-Dec-14 A | 30-Dec-14 A | |
| L11-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 30-Dec-14 A | 31-Dec-14 A | |
| I-5302 | Heat Pump Revision - rework MEP at celing | 5 | 0 | 30-Dec-14 A | 12-Jan-15 A | |
| I-1606 | Manlift finishes - Prime & paint | 4 | 0 | 31-Dec-14 A | 06-Jan-15 A | |
| L07-7136 | Install Door and Hardware | 1 | 0 | 31-Dec-14 A | 31-Dec-14 A | |
| L12-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 31-Dec-14 A | 05-Jan-15 A | |
| CO-7214 | Cx - Flush & Fill HVAC Hydronics Systems | 5 | 0 | 02-Jan-15 A | 05-Jan-15 A | |
| MPP-1032 | (C) Elevation 23/24/25 (Porte Cochere north, below c | 5 | 0 | 02-Jan-15 A | 19-Jan-15 A | |
| L1BOH2-8215 | GWB tape & finish walls & ceilings | 7 | 1 | 05-Jan-15 A | 16-Feb-15 | 10 |
| L10-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| L11-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 13-Jan-15 A | |
| L12-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 13-Jan-15 A | |
| L14-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| L16-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L04-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L05-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L06-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L05-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| L06-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L07-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L08-7136 | Install Door and Hardware | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L08-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L09-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L10-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L14-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| SW-2314 | Zone 3 - FRP sidewalk | 5 | 1 | 05-Jan-15 A | 16-Feb-15 | 30 |

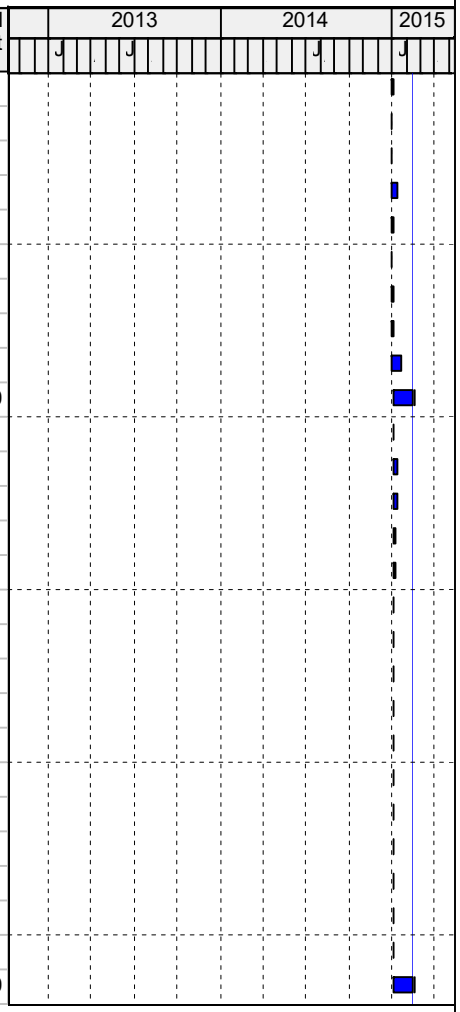



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 05-Jan-15 A | 27-Jan-15 A | |
| CO-7240 | Cx - Heat Pump Start-Up - Levels 3 & 4 | 5 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| SW-2220 | Zone 2 - FRP curb/gutter at NW corner | 4 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| MPT-1054 | Complete Elevation 30 (south elevation, west of man | 5 | 1 | 05-Jan-15 A | 16-Feb-15 | 16 |
| MPP-1028 | (C) Tapered pilasters, west | 3 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| MPP-1030 | (C) Tapered pilasters, east | 3 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| LL2-8142 | HVAC drops/trim to grid | 3 | 0 | 05-Jan-15 A | 19-Jan-15 A | |
| L1L-8216 | Complete electrical/fire alarm drops @ ceilings | 5 | 0 | 05-Jan-15 A | 08-Jan-15 A | |
| L1BOH2-8217 | GWB hang ceilings and at heat pumps | 10 | 0 | 05-Jan-15 A | 29-Jan-15 A | |
| L1L-8222 | Complete HVAC drops @ ceilings | 5 | 0 | 05-Jan-15 A | 23-Jan-15 A | |
| L1L-8224 | Complete fire sprinkler drops @ ceilings | 5 | 0 | 05-Jan-15 A | 08-Jan-15 A | |
| L1L-8254 | Complete electrical rough-in at walls | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| I-5350 | Fabricate & install new hydraulic ram | 30 | 0 | 05-Jan-15 A | 29-Jan-15 A | |
| SW-2226 | Zone 2 - Procure light poles and replacement luminai | 25 | 5 | 05-Jan-15 A | 20-Feb-15 | 21 |
| LL1-8120 | Complete GWB tape & finish in corridors | 7 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| L1K-8108 | Complete kitchen hood installation and fire blanket w | 10 | 0 | 05-Jan-15 A | 05-Feb-15 A | |
| L1K-8110 | Complete MEP rough-in above ceiling | 10 | 0 | 05-Jan-15 A | 05-Feb-15 A | |
| L1B-8122 | Framing, complete ceiling at corridors | 5 | 0 | 05-Jan-15 A | 13-Jan-15 A | |
| I-5102 | Bar lighting layout - resolve conflicts (RFI) | 7 | 0 | 05-Jan-15 A | 19-Jan-15 A | |
| I-5110 | Bar radius ceiling - resolve framing issues | 5 | 0 | 05-Jan-15 A | 14-Jan-15 A | |
| I-5120 | Dining feature wall - resolve design issues | 7 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| L02-8178 | Complete heat pump enclosures | 5 | 0 | 05-Jan-15 A | 12-Jan-15 A | |
| I-5850 | Owner provide revised lighting layout | 10 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| I-5130 | Bar plumbing relocation - resolve conflicts | 25 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| I-5140 | Damper at BPF #8 - resolve conflicts | 30 | 0 | 05-Jan-15 A | 29-Jan-15 A | |
| I-5150 | Sprinkler pipe furring - resolve conflicts | 15 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| I-5160 | ASI 63 electrical revisions - resolve conflicts | 10 | 0 | 05-Jan-15 A | 16-Jan-15 A | |

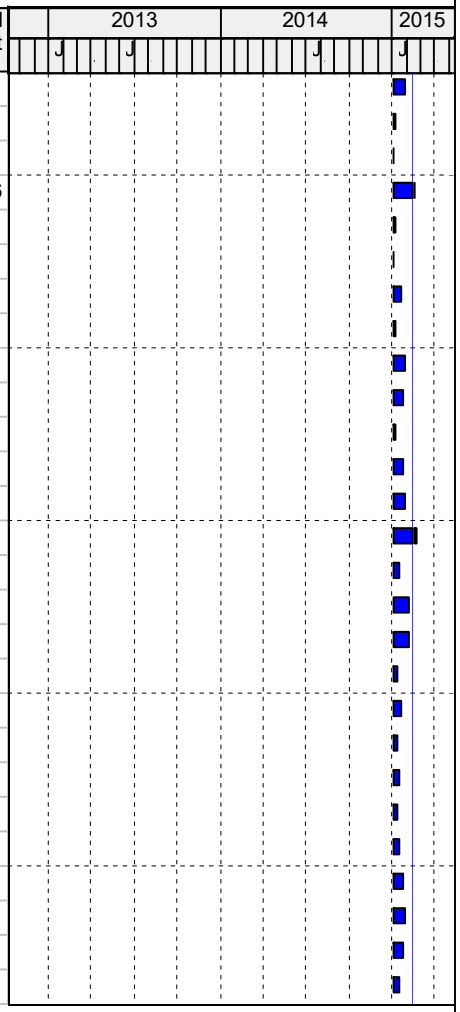



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 06-Jan-15 A | 07-Jan-15 A | |
| L07-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L08-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L09-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L10-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L09-7136 | Install Door and Hardware | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L10-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L11-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L12-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L15-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 06-Jan-15 A | 07-Jan-15 A | |
| L11-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 06-Jan-15 A | 12-Jan-15 A | |
| L03-8660 | GWB hang ceilings at Pool | 3 | 0 | 06-Jan-15 A | 04-Feb-15 A | |
| L1K-6011 | Complete HVAC RI @ ceilings | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L1K-6013 | Complete electrical rough-in @ ceilings & inspection | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L1K-6015 | Complete fire sprinkler RI @ ceilings | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L12-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L14-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L15-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L16-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L15-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 07-Jan-15 A | 20-Jan-15 A | |
| L12-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 07-Jan-15 A | 13-Jan-15 A | |
| CO-7242 | Cx - Heat Pump Start-Up - Levels 5 & 6 | 5 | 0 | 07-Jan-15 A | 09-Jan-15 A | |
| CO-7252 | Cx - Start-Up - FSD & SD Operation Verification | 10 | 0 | 07-Jan-15 A | 22-Jan-15 A | |
| MPP-1026 | Complete Elevation 7/8 (east elevation) | 5 | 1 | 07-Jan-15 A | 16-Feb-15 | 35 |
| LL1-6014lb2 | L1 bar redesign - GWB hang, tape, finish (including ir | 12 | 0 | 08-Jan-15 A | 30-Jan-15 A | |
| SW-2310 | Zone 3 - Install irrigation sleeves | 2 | 0 | 08-Jan-15 A | 08-Jan-15 A | |
| I-1638 | Manlift finishes - ceiling grid | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |

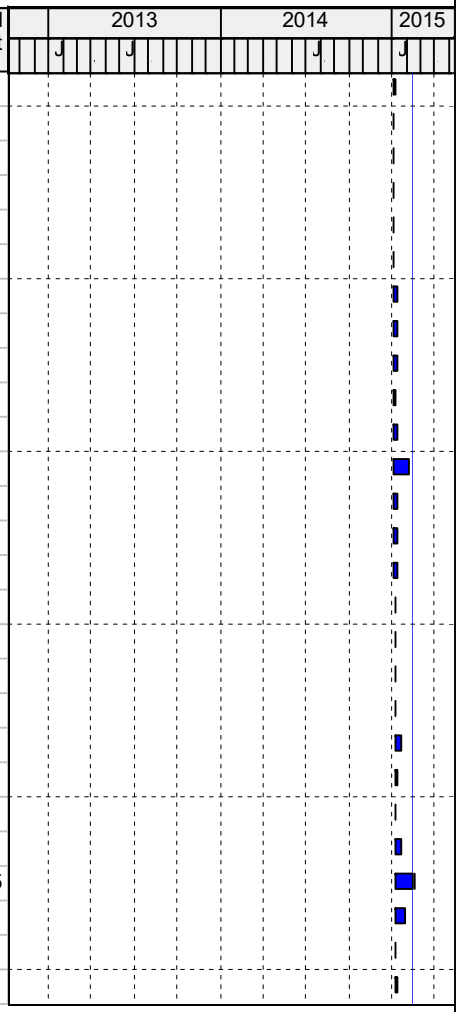



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8662 | GWB tape & finish walls & ceilings at Pool | 7 | 7 | 08-Jan-15 A | 24-Feb-15 | 11 |
| MPT-1072 | Tower Sign, West (El, 52) | 5 | 2 | 08-Jan-15 A | 19-Feb-15 | 37 |
| L1L-8220 | Complete fire sprinkler RI @ ceilings | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| L1L-8270 | Complete HVAC RI @ ceilings | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| SW-2224 | Zone 2 - Adjust Comcast vault lids | 2 | 0 | 08-Jan-15 A | 08-Jan-15 A | |
| I-1212 | Resolve stud/duct conflict at east wall | 5 | 0 | 08-Jan-15 A | 14-Jan-15 A | |
| L04-8218 | Install base at corridors (& approve mockup) | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| GB410-100 | Complete GWB - Levels 4-10 | 5 | 0 | 08-Jan-15 A | 14-Jan-15 A | |
| LL1-6014Ib4 | L1 bar redesign - complete reframing | 5 | 0 | 08-Jan-15 A | 19-Jan-15 A | |
| I-5306 | Heat Pump Revision - complete reframing | 5 | 0 | 08-Jan-15 A | 19-Jan-15 A | |
| L15-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L16-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8121 | Install Bathroom "Barn Doors" | 3 | 1 | 12-Jan-15 A | 17-Feb-15 | 26 |
| L04-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L05-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L06-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L07-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L08-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L09-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L10-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L11-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L12-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L14-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L15-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L11-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |

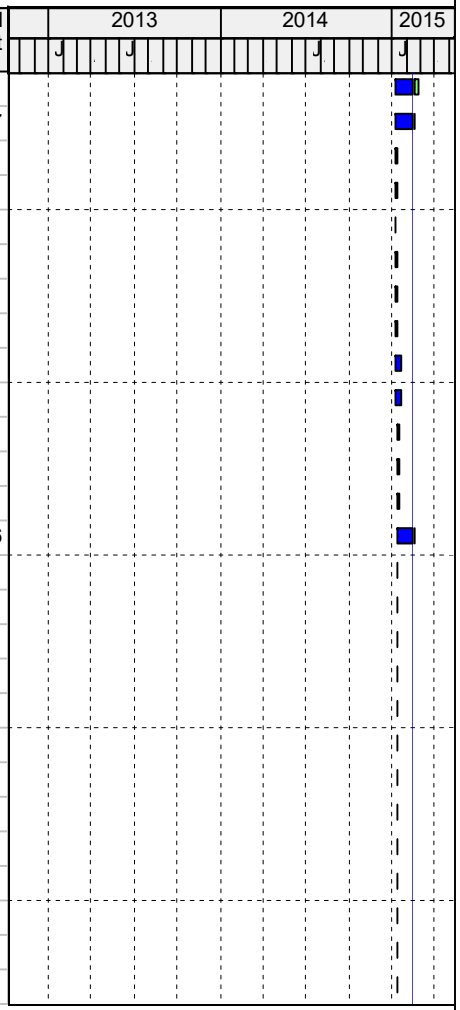



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-7136 | Install doors & hardware | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L14-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L15-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L15-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L14-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L11-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L03-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 12-Jan-15 A | 19-Jan-15 A | |
| CO-7244 | Cx - Heat Pump Start-Up - Levels 7 & 8 | 5 | 0 | 12-Jan-15 A | 14-Jan-15 A | |
| MPT-1068 | Tower Sign, North (El. 51) | 5 | 2 | 12-Jan-15 A | 17-Feb-15 | 37 |
| L03-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L11-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L14-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L15-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L02-8144 | GWB hang at Locker Rooms | 2 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| SW-2326 | Zone 3 - Install j-boxes | 3 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| I-5800 | Mechanical correction notice - interference with light t | 10 | 0 | 12-Jan-15 A | 13-Feb-15 A | |
| I-5602 | Frame FCC ceiling | 2 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| CO-7166 | Replace exhaust fitting | 10 | 0 | 12-Jan-15 A | 28-Jan-15 A | |
| MPP-1034 | Deliver Elevation 48 corner panels | 25 | 6 | 12-Jan-15 A | 23-Feb-15 | 35 |
| MPP-1042 | Deliver Elevation 32 corner panels | 25 | 0 | 12-Jan-15 A | 02-Feb-15 A | |
| MPP-1066 | Deliver Elevation 33/34 corner panels | 25 | 6 | 12-Jan-15 A | 23-Feb-15 | 20 |
| MPP-1068 | Deliver Elevation 32 spandrel panel head/sill flashings | 25 | 0 | 12-Jan-15 A | 13-Feb-15 A | |
| MPP-1070 | Deliver Elevation 44 spandrel panel head/sill flashings | 25 | 0 | 12-Jan-15 A | 13-Feb-15 A | |
| MPP-1072 | Deliver remaining Elevation 4 panels | 25 | 0 | 12-Jan-15 A | 06-Feb-15 A | |
| MPP-1074 | Deliver remaining Elevation 7 panels | 25 | 0 | 12-Jan-15 A | 06-Feb-15 A | |

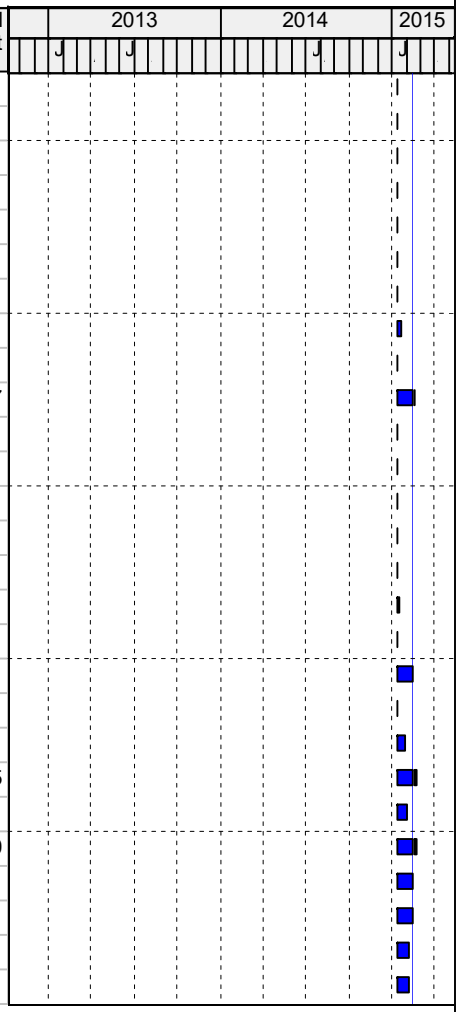



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPP-1076 | Deliver Pool cornice panels | 25 | 5 | 12-Jan-15 A | 20-Feb-15 | 17 |
| L15-7136 | Install doors & hardware | 1 | 1 | 13-Jan-15 A | 16-Feb-15 | 55 |
| L03-8664 | Paint, prime & first coat finish at Pool | 3 | 3 | 13-Jan-15 A | 27-Feb-15 | 11 |
| MPP-1022 | (A) Complete Elevation 40 (pool south elevation, L3-L | 5 | 0 | 13-Jan-15 A | 20-Jan-15 A | |
| L05-8226 | Install base at corridors | 1 | 0 | 13-Jan-15 A | 13-Jan-15 A | |
| L16-8138 | Bathrooms - Install toilet accessories | 2 | 0 | 14-Jan-15 A | 15-Jan-15 A | |
| L14-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| CO-7246 | Cx - Heat Pump Start-Up - Levels 9 & 10 | 5 | 0 | 14-Jan-15 A | 16-Jan-15 A | |
| I-5604 | GWB hang, tape & finish FCC ceiling | 5 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| L14-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 15-Jan-15 A | 16-Jan-15 A | |
| L16-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 15-Jan-15 A | 21-Jan-15 A | |
| SW-2126 | Zone 1 - Remove temporary transformer | 5 | 0 | 15-Jan-15 A | 28-Jan-15 A | |
| I-5112 | Bar radius ceiling - complete framing | 5 | 0 | 15-Jan-15 A | 20-Jan-15 A | |
| L07-8226 | Install base at corridors | 1 | 0 | 16-Jan-15 A | 16-Jan-15 A | |
| L16-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| CO-7248 | Cx - Heat Pump Start-Up - Levels 11 & 12 | 5 | 0 | 19-Jan-15 A | 21-Jan-15 A | |
| CO-7254 | Cx - Start-Up - MUA AAON (8) | 5 | 2 | 19-Jan-15 A | 17-Feb-15 | 21 |
| SW-2020 | Porte Cochere - EIFS at ceiling | 7 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L02-8146 | GWB tape & finish at Locker Rooms | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L1K-8138 | Complete GWB hang & tape | 9 | 0 | 19-Jan-15 A | 06-Feb-15 A | |
| L1L-8252 | Complete electrical/fire alarm rough-in @ ceilings | 3 | 0 | 19-Jan-15 A | 26-Jan-15 A | |
| LL1-8122 | Paint corridors | 6 | 0 | 19-Jan-15 A | 21-Jan-15 A | |
| L1B-6027 | Framing, ceiling at East Ballroom | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L09-8226 | Install base at corridors | 1 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| GB410-102 | Complete painting - Levels 4-10 | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL1-Z2-8110 | Paint, prime & first coat finish at Meeting Rooms | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| I-5122 | Dining feature wall - complete framing | 3 | 0 | 19-Jan-15 A | 21-Jan-15 A | |

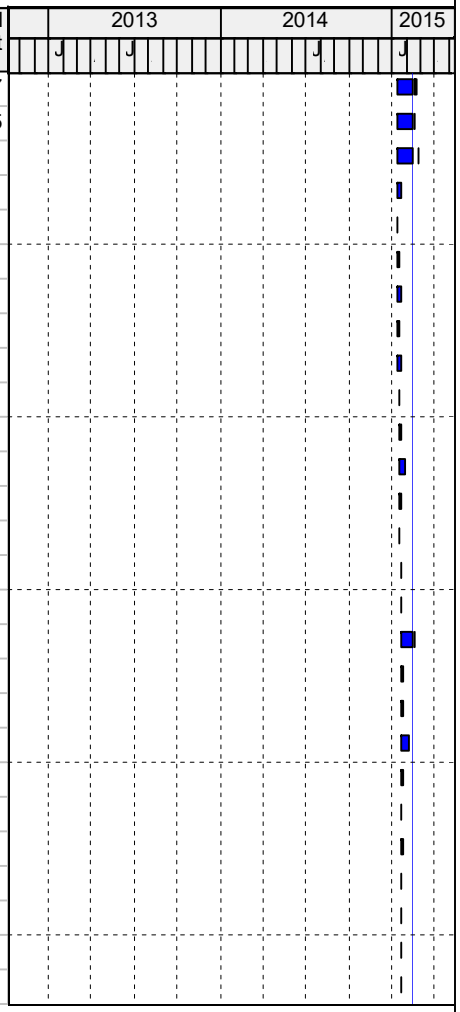



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-5162 | ASI 63 electrical revisions - demo existing | 1 | 0 | 19-Jan-15 A | 19-Jan-15 A | |
| L1B-8170 | Complete cover inspections | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L17-8138 | Bathrooms - Install toilet accessories | 2 | 1 | 20-Jan-15 A | 18-Feb-15 | 30 |
| MPP-1014 | Caulking - Elevation 1/2/A/B/C/23/24/25 (west elevati | 9 | 0 | 20-Jan-15 A | 30-Jan-15 A | |
| CO-7232 | Cx - TAB - CW Pump Totalization | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| L03-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| LL1-8202 | HVAC trim at ceiling | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| LL1-8206 | Lighting & electrical trim | 4 | 0 | 20-Jan-15 A | 28-Jan-15 A | |
| LL1-8208 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| LL1-Z2-8138 | Paint corridors | 3 | 0 | 20-Jan-15 A | 04-Feb-15 A | |
| L10-8226 | Install base at corridors | 1 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| GB410-106 | Complete flooring - Levels 4-10 | 3 | 0 | 20-Jan-15 A | 26-Jan-15 A | |
| L04-8422 | Floor prep | 1 | 0 | 20-Jan-15 A | 02-Feb-15 A | |
| I-5606 | Paint FCC ceiling | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| I-5104 | Bar lighting layout - complete elecrical rough-in | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| I-5164 | ASI 63 electrical revisions - revise electrical | 3 | 0 | 20-Jan-15 A | 02-Feb-15 A | |
| L16-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| CO-7234 | Cx - TAB - CW Water Balancing | 10 | 10 | 21-Jan-15 A | 27-Feb-15 | 39 |
| L15-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L14-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L12-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L11-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L16-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| CO-7250 | Cx - Heat Pump Start-Up - Levels 14 & 15 | 5 | 0 | 21-Jan-15 A | 23-Jan-15 A | |
| L16-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| I-5304 | Heat Pump Revision - rework GWB | 9 | 0 | 21-Jan-15 A | 30-Jan-15 A | |
| L03-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |

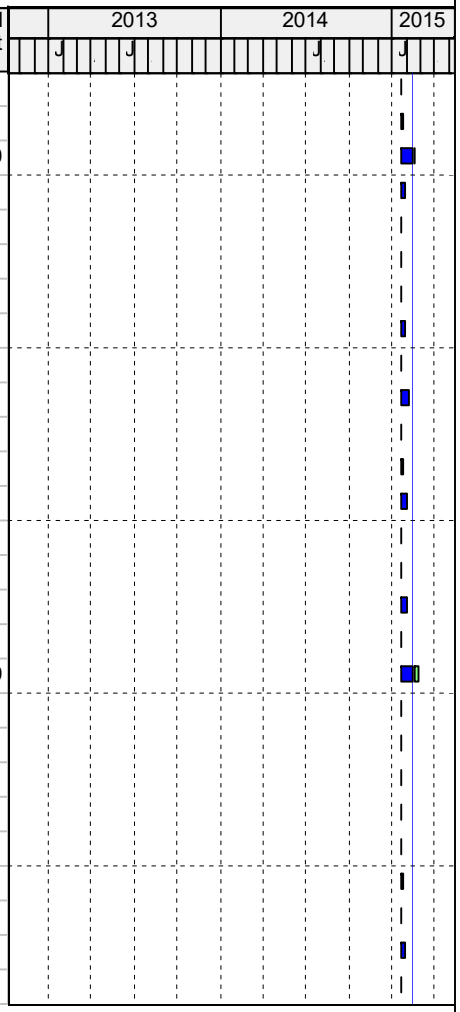



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L05-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L06-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L07-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L08-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L09-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L11-8226 | Install base at corridors | 1 | 0 | 21-Jan-15 A | 22-Jan-15 A | |
| L05-8422 | Floor prep | 1 | 0 | 21-Jan-15 A | 02-Feb-15 A | |
| L07-7134 | Flooring - VCT | 1 | 0 | 22-Jan-15 A | 22-Jan-15 A | |
| L17-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 22-Jan-15 A | 27-Jan-15 A | |
| LL1-8210 | Fire sprinkler trim | 1 | 0 | 22-Jan-15 A | 22-Jan-15 A | |
| L12-8226 | Install base at corridors | 1 | 0 | 22-Jan-15 A | 23-Jan-15 A | |
| L05-7134 | Flooring - VCT | 1 | 0 | 23-Jan-15 A | 23-Jan-15 A | |
| MPP-1016 | Caulking - Elevation 7/8 (east elevation) | 8 | 6 | 23-Jan-15 A | 24-Feb-15 | 29 |
| LL1-Z2-8120 | GWB hang, tape & finish ceiling clouds at Jr. Ballroon | 7 | 2 | 23-Jan-15 A | 17-Feb-15 | 14 |
| LL1-Z3-8148 | Paint Restrooms | 3 | 0 | 23-Jan-15 A | 26-Jan-15 A | |
| MPT-1104 | (B) Install alcoves, east (Elev. 7/8) | 2 | 0 | 23-Jan-15 A | 09-Feb-15 A | |
| L06-8422 | Floor prep | 1 | 0 | 23-Jan-15 A | 23-Jan-15 A | |
| L17-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L06-7134 | Flooring - VCT | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| CO-7216 | Cx - Start-Up Fluid Cooler (power, pre-start & start) | 3 | 0 | 26-Jan-15 A | 28-Jan-15 A | |
| L16-8140 | Install window sills | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| L04-8224 | HVAC grilles & registers at corridors | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| MPT-1058 | Elevation 32 hat channel (south elevation, east of ma | 3 | 1 | 26-Jan-15 A | 17-Feb-15 | 16 |
| MPT-1090 | Caulking - Elevation 40 (pool south elevation, L3-L17 | 9 | 0 | 26-Jan-15 A | 05-Feb-15 A | |
| LL1-8123 | Floor prep | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| SW-2052 | Zone 4 - Waterproof NW planter walls | 4 | 0 | 26-Jan-15 A | 29-Jan-15 A | |

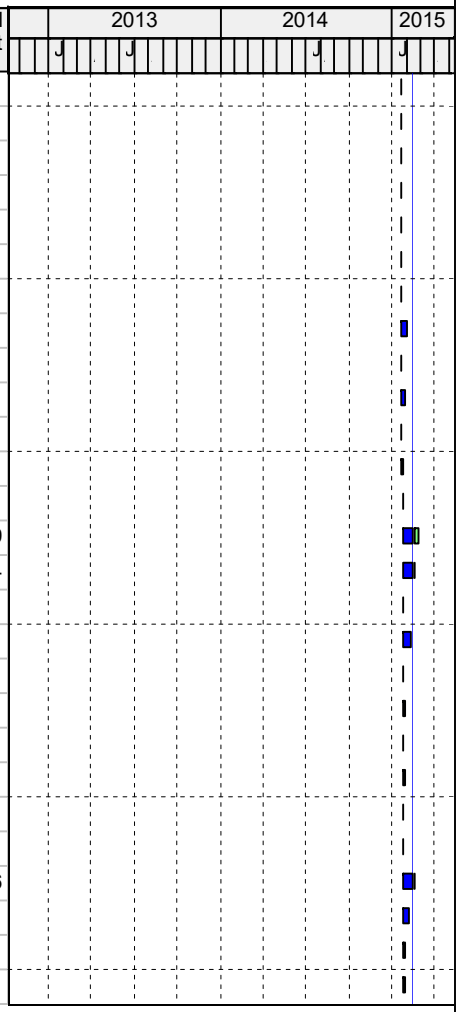



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8290 | GWB, top rock | 3 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L10-8131 | Bathrooms - Install access panels | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| L14-8226 | Install base at corridors | 1 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| I-5372 | (S) Elevation 32, complete insulation | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| GB1117-100 | Complete GWB - Levels 3, 11-17 | 7 | 7 | 26-Jan-15 A | 24-Feb-15 | 14 |
| SW-2322 | Zone 3 - FRP landscape curb at exit door | 5 | 0 | 26-Jan-15 A | 30-Jan-15 A | |
| I-6010 | RFI 901 - Pool topping slab issue | 10 | 1 | 26-Jan-15 A | 16-Feb-15 | 2 |
| L03-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L16-7034 | Install doors & hardware (x42) | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L17-7034 | Install doors & hardware (x42) | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L08-7134 | Flooring - VCT | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L16-7138 | Electrical trim & finish | 1 | 1 | 27-Jan-15 A | 16-Feb-15 | 30 |
| L17-7136 | Install doors & hardware | 1 | 1 | 27-Jan-15 A | 18-Feb-15 | 55 |
| I-1640 | Manlift finishes - Install window sills | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L03-8668 | Remove scaffolding at pool pit | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L17-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L11-8131 | Bathrooms - Install access panels | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L15-8226 | Install base at corridors | 1 | 0 | 27-Jan-15 A | 28-Jan-15 A | |
| MPP-1052 | (B) Elevation 3 (south elevation, west of manlift, L1-L: | 5 | 0 | 27-Jan-15 A | 30-Jan-15 A | |
| GB410-108 | Complete base - Levels 4-10 | 4 | 0 | 27-Jan-15 A | 30-Jan-15 A | |
| L08-8422 | Floor prep | 1 | 0 | 27-Jan-15 A | 28-Jan-15 A | |
| I-5132 | Bar plumbing relocation - relocate waste line | 3 | 0 | 27-Jan-15 A | 29-Jan-15 A | |
| I-5152 | Sprinkler pipe furring - install framing around pipe | 2 | 0 | 27-Jan-15 A | 28-Jan-15 A | |
| L09-7134 | Flooring - VCT | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L17-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L17-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| EL-6042 | Elev 6 - Install EMR heat pump | 6 | 3 | 28-Jan-15 A | 18-Feb-15 | 32 |

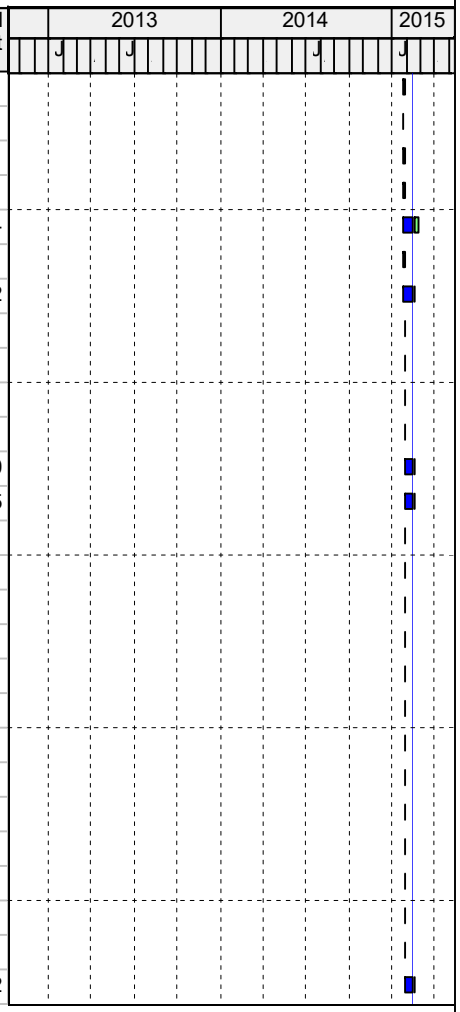



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPT-1056 | Complete Elevation 31 (above L12 terrace, west elev | 3 | 0 | 28-Jan-15 A | 13-Feb-15 A | |
| L1L-8256 | GWB hang walls | 3 | 0 | 28-Jan-15 A | 05-Feb-15 A | |
| SW-2230 | Zone 2 - Repair sidewalk north of 3rd Ave | 5 | 0 | 28-Jan-15 A | 30-Jan-15 A | |
| L12-8131 | Bathrooms - Install access panels | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L08-8226 | Install base at corridors | 1 | 0 | 28-Jan-15 A | 30-Jan-15 A | |
| L16-8226 | Install base at corridors | 1 | 0 | 28-Jan-15 A | 29-Jan-15 A | |
| I-5373 | (S) Elevation 32, install sign backing | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L07-8422 | Floor prep | 1 | 0 | 28-Jan-15 A | 03-Feb-15 A | |
| I-6000 | Resolve cloud framing engineering issue | 5 | 0 | 28-Jan-15 A | 03-Feb-15 A | |
| L10-7134 | Flooring - VCT | 1 | 0 | 29-Jan-15 A | 29-Jan-15 A | |
| L1L-8226 | GWB hang ceilings & complete walls | 3 | 1 | 29-Jan-15 A | 16-Feb-15 | 4 |
| L1L-8248 | Complete electrical/fire alarm rough-in @ ceilings | 3 | 0 | 29-Jan-15 A | 02-Feb-15 A | |
| L1L-8250 | Complete HVAC RI @ ceilings | 5 | 0 | 29-Jan-15 A | 04-Feb-15 A | |
| L03-8218 | Install base at corridors | 1 | 0 | 29-Jan-15 A | 30-Jan-15 A | |
| MPP-1062 | (C) Install level 3 cornice metal (Porte Cochere) | 2 | 0 | 29-Jan-15 A | 04-Feb-15 A | |
| EL-6040 | Elev 6 - Install machine room controller equipment/hy | 3 | 2 | 30-Jan-15 A | 17-Feb-15 | 30 |
| EL-6054 | Elev 6 - Install EMR doors, hardware & labeling | 2 | 1 | 30-Jan-15 A | 16-Feb-15 | 33 |
| LL1-8160 | Flooring - carpet | 10 | 4 | 30-Jan-15 A | 19-Feb-15 | 16 |
| I-5472 | Reframe Laundry Room ceiling (per ceiling height RF | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5474 | Restore Laundry Room GWB (hang & tape) (per ceili | 5 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5476 | Repaint Laundry Room ceiling | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5478 | Demo existing Laundry Room ceiling | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5480 | Revise MEP above Laundry Room ceiling | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5134 | Bar plumbing relocation - adust framing | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5136 | Bar plumbing relocation - GWB hang, tape & finish [D | 7 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5138 | Bar plumbing relocation - paint [DELETED] | 2 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5142 | Damper at BPF #8 - mechanical revisions | 2 | 0 | 30-Jan-15 A | 02-Feb-15 A | |

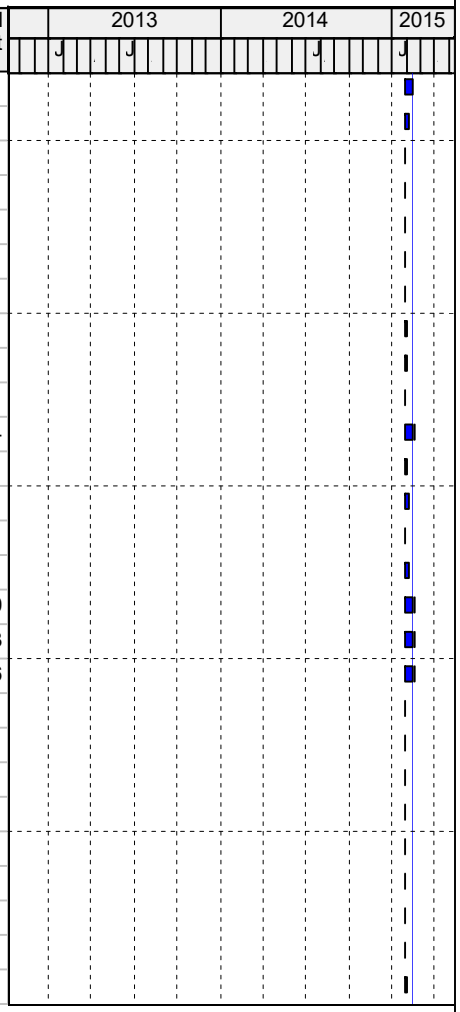



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 02-Feb-15 A | 02-Feb-15 A | |
| L04-7134 | Flooring - VCT | 1 | 0 | 02-Feb-15 A | 02-Feb-15 A | |
| LL1-8124a | Install base | 10 | 3 | 02-Feb-15 A | 18-Feb-15 | 18 |
| CO-7218 | Cx - Heat Pump Start-Up - Levels 16 & 17 | 5 | 0 | 02-Feb-15 A | 04-Feb-15 A | |
| LL1-6014Id | L1 bar redesign - paint ceilings at Excercise & MR9 | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| EL-1236 | Elev 1&2 - Walsh/TKE pre-inspection | 6 | 0 | 02-Feb-15 A | 06-Feb-15 A | |
| MPT-1050 | (B) Install louvers, east | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| MPT-1070 | Tower Sign, East (El. 44) | 5 | 0 | 02-Feb-15 A | 10-Feb-15 A | |
| L1L-8272 | GWB hang ceilings | 3 | 0 | 02-Feb-15 A | 04-Feb-15 A | |
| SW-2320 | Zone 3 - Pour ped pole base | 3 | 0 | 02-Feb-15 A | 05-Feb-15 A | |
| LL1-8156 | Install doors & hardware at corridors | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| L1B-6015 | HVAC drops at West Ballrooms | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L1B-6021 | Electrical drops at West Ballrooms | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L1B-6029 | HVAC drops at East Ballroom | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L1B-6031 | Electrical drops at East Ballroom | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L06-8226 | Install base at corridors | 1 | 0 | 02-Feb-15 A | 02-Feb-15 A | |
| GB410-104 | Complete vinyl wallcoverings - Levels 4-10 | 4 | 2 | 02-Feb-15 A | 17-Feb-15 | 15 |
| SW-2234 | Zone 2 - FRP door curbs | 4 | 0 | 02-Feb-15 A | 05-Feb-15 A | |
| L05-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L04-7138 | Electrical trim & finish | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L05-7138 | Electrical trim & finish | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L11-7134 | Flooring - VCT | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| SW-2022 | Zone 4 - Remove pedestrian protection on 110th Ave | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L1L-8246 | Complete fire sprinkler RI @ ceilings | 2 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| LL1-8184 | Install storefront at Exercise Room | 1 | 1 | 03-Feb-15 A | 16-Feb-15 | 9 |
| L12-8422 | Floor prep | 1 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| L14-8422 | Floor prep | 1 | 0 | 03-Feb-15 A | 04-Feb-15 A | |

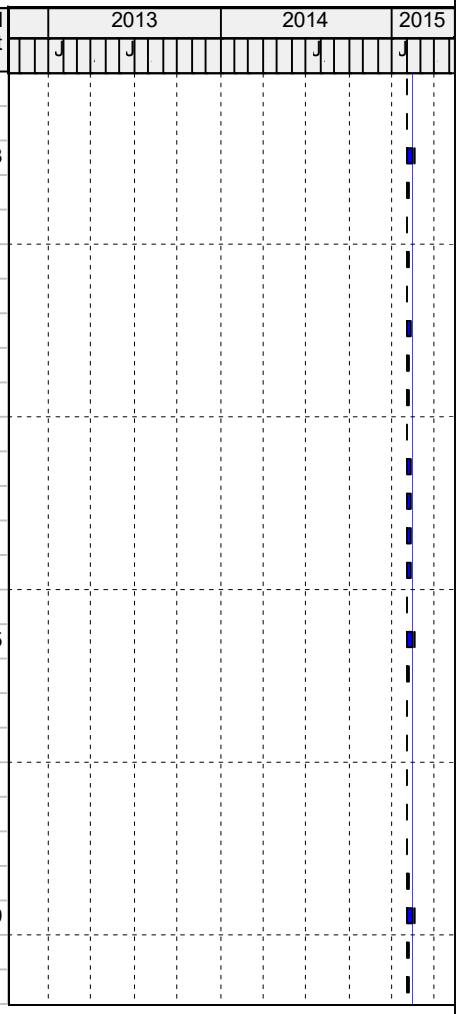


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8422 | Floor prep | 1 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| I-5144 | Damper at BPF #8 - framing revisions | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| I-5154 | Sprinkler pipe furring - GWB hang | 7 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| I-5166 | ASI 63 electrical revisions - insulation | 2 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| L06-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 04-Feb-15 A | 04-Feb-15 A | |
| L12-7134 | Flooring - VCT | 1 | 0 | 04-Feb-15 A | 04-Feb-15 A | |
| LL1-Z3-8142 | Ceramic tile in restrooms | 7 | 1 | 04-Feb-15 A | 16-Feb-15 | 21 |
| L1K-8144 | Paint, prime & first coat finish | 3 | 1 | 04-Feb-15 A | 16-Feb-15 | 25 |
| LL1-Z2-8158 | Wall coverings - vinyl at Meeting Rooms | 2 | 0 | 04-Feb-15 A | 05-Feb-15 A | |
| L09-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 06-Feb-15 A | |
| L10-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 09-Feb-15 A | |
| L11-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 09-Feb-15 A | |
| L16-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 10-Feb-15 A | |
| I-5146 | Damper at BPF #8 - complete GWB hang | 1 | 0 | 04-Feb-15 A | 04-Feb-15 A | |
| I-5168 | ASI 63 electrical revisions - vapor barrier | 2 | 0 | 04-Feb-15 A | 05-Feb-15 A | |
| L07-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 05-Feb-15 A | 05-Feb-15 A | |
| L14-7134 | Flooring - VCT | 1 | 0 | 05-Feb-15 A | 05-Feb-15 A | |
| L1L-8102a | GWB tape & finish walls & ceilings (Dining & Lounge) | 7 | 0 | 05-Feb-15 A | 12-Feb-15 A | |
| LL1-8170 | Flooring - tile at elevator lobby | 3 | 0 | 05-Feb-15 A | 09-Feb-15 A | |
| LL1-8186 | Wall coverings - vinyl at corridors | 5 | 2 | 05-Feb-15 A | 19-Feb-15 | 17 |
| L1B-6023 | Fire sprinkler drops at West Ballrooms | 5 | 0 | 05-Feb-15 A | 09-Feb-15 A | |
| L1B-6033 | Fire sprinkler drops at East Ballroom | 5 | 0 | 05-Feb-15 A | 09-Feb-15 A | |
| I-6100 | Resolve lighting/access panel conflict | 5 | 0 | 05-Feb-15 A | 13-Feb-15 A | |
| L08-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 06-Feb-15 A | 06-Feb-15 A | |
| L15-7134 | Flooring - VCT | 1 | 0 | 06-Feb-15 A | 06-Feb-15 A | |
| MPP-1054 | Caulking - Elevation 3 (south elevation, west of manli | 3 | 0 | 06-Feb-15 A | 10-Feb-15 A | |
| L03-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 09-Feb-15 A | 09-Feb-15 A | |

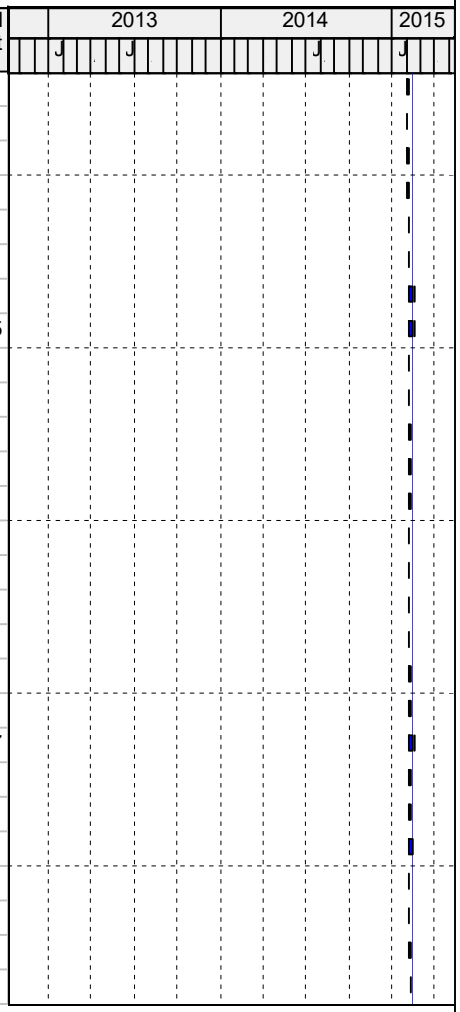



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8408 | Install base at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L05-8408 | Install base at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L06-8408 | Install base at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L09-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L16-7134 | Flooring - VCT | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L1K-8102a | GWB hang ceilings at Public Restroom | 2 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| LL2-2094 | Install doors & hardware at Laundry | 2 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| SW-2032 | Zone 4 - Demo existing trees & hardscapes | 3 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| CO-7139 | Install remaining devices & prep devices for testing - | 7 | 2 | 09-Feb-15 A | 17-Feb-15 | 16 |
| MPP-1024 | (B) Complete Elevation 4 (south elevation, east of tov | 2 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| L1L-8218 | Frame ceilings & inspection | 5 | 0 | 09-Feb-15 A | 12-Feb-15 A | |
| L1K-8136 | Ceiling grid & inspection | 4 | 0 | 09-Feb-15 A | 11-Feb-15 A | |
| L1L-8274 | GWB tape & finish walls & ceilings | 7 | 2 | 09-Feb-15 A | 17-Feb-15 | 16 |
| L15-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L16-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L17-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L14-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| I-5170 | ASI 63 electrical revisions - GWB hang, tape & finish | 7 | 2 | 09-Feb-15 A | 17-Feb-15 | 3 |
| SW-2058 | Zone 4 - Demo existing curb at 110th | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| MPT-1114 | Cap metal - Porte Cochere | 3 | 0 | 09-Feb-15 A | 12-Feb-15 A | |
| I-5172 | Resolve Bar Area RFIs | 10 | 5 | 09-Feb-15 A | 20-Feb-15 | 1 |
| L07-8408 | Install base at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L08-8408 | Install base at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L09-8408 | Install base at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L10-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L11-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L17-7134 | Flooring - VCT | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |

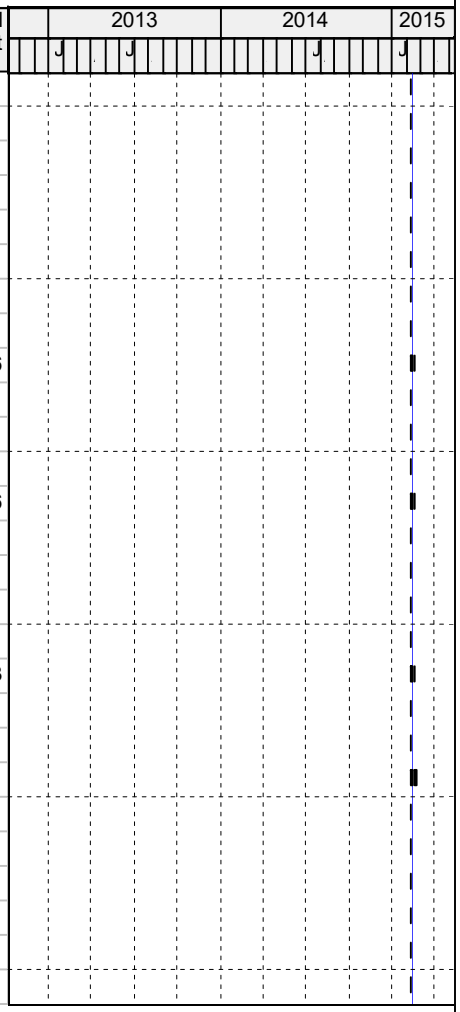



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8224 | HVAC grilles & registers at corridors | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L08-8224 | HVAC grilles & registers at corridors | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L07-8224 | HVAC grilles & registers at corridors | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| SW-2036 | Zone 4 - Grade for curb and gutter | 2 | 0 | 10-Feb-15 A | 11-Feb-15 A | |
| CO-7140 | Fire Alarm System Device Testing - Tower Levels 4 thr | 7 | 3 | 10-Feb-15 A | 18-Feb-15 | 16 |
| L17-8422 | Floor prep | 1 | 0 | 10-Feb-15 A | 11-Feb-15 A | |
| MPT-1116 | Cap metal - Pool high roof | 3 | 0 | 10-Feb-15 A | 12-Feb-15 A | |
| L10-8408 | Install base at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L11-8408 | Install base at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L12-8408 | Install base at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L12-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L14-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L03-7134 | Flooring - VCT | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| MPT-1018a | Install hi-roof cornice metal | 8 | 5 | 11-Feb-15 A | 20-Feb-15 | 43 |
| SW-2038 | Zone 4 - FRP curb & gutter | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| SW-2046 | Zone 4 - Install conduit | 2 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L1K-8152 | Install doors & hardware | 3 | 2 | 11-Feb-15 A | 18-Feb-15 | 27 |
| L1L-8228 | GWB tape & finish | 7 | 4 | 11-Feb-15 A | 20-Feb-15 | 4 |
| SW-2054 | Zone 4 - Install flag pole bases | 3 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| L17-8226 | Install base at corridors | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| MPP-1058 | (B) Install podium cornice, south/east | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| L03-8422 | Floor prep | 1 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| MPT-1108 | Cap metal - complete at tower | 5 | 0 | 11-Feb-15 A | 13-Feb-15 A | |
| MPT-1112 | Cap metal - complete at Ballroom roof | 3 | 0 | 11-Feb-15 A | 13-Feb-15 A | |
| L14-8408 | Install base at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L15-8408 | Install base at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L15-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |

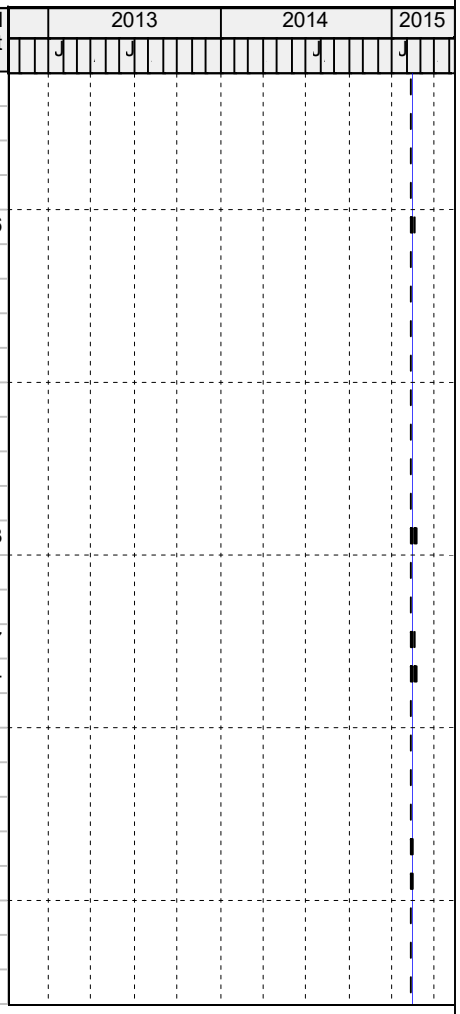



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8408 | Install base at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L16-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L06-7138 | Electrical trim & finish | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L1K-8102b | GWB tape & finish at Restrooms | 7 | 4 | 12-Feb-15 A | 19-Feb-15 | 1 |
| LL1-8154 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 2 | 12-Feb-15 A | 19-Feb-15 | 17 |
| L17-8408 | Install base at Elevator Lobby | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| L17-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| SW-2118 | Zone 1 - FRP sidewalk (NE & SE corners) | 2 | 1 | 13-Feb-15 A | 05-Mar-15 | 27 |
| SW-2034 | Zone 4 - Install irrigation sleeves | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| SW-2060 | Zone 4 - Sawcut curb & gutter | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| CO-7100T | Cx - Start-Up - Life Safety Exhaust Fans and VFD's | 13 | 13 | 16-Feb-15 | 04-Mar-15 | 18 |
| CO-7102T | Cx - DDC Point-To-Point - Central Plant | 5 | 5 | 16-Feb-15 | 20-Feb-15 | 44 |
| L03-7034 | Install doors & hardware (x42) | 1 | 1 | 16-Feb-15* | 16-Feb-15 | 27 |
| L03-7136 | Install doors & hardware | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 22 |
| L11-7032 | Flooring - VCT (x42) | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 26 |
| L07-7138 | Electrical trim & finish | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 13 |
| L08-7138 | Electrical trim & finish | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 15 |
| L09-7138 | Electrical trim & finish | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 13 |
| L10-7138 | Electrical trim & finish | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 15 |
| L11-7138 | Electrical trim & finish | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 14 |
| L12-7138 | Electrical trim & finish | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 16 |
| L14-7138 | Electrical trim & finish | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 26 |
| L15-7138 | Electrical trim & finish | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 28 |
| MPP-1012 | Caulking - Elevation 4 (south elevation, east of tower) | 6 | 6 | 16-Feb-15 | 23-Feb-15 | 40 |
| CO-7160 | Generator - Cx generator/owner training | 3 | 3 | 16-Feb-15 | 18-Feb-15 | 55 |
| CO-7400 | Cx - 3rd Party Cx of Mechanical, Plumbing, Electrical | 40 | 40 | 16-Feb-15 | 10-Apr-15 | 18 |
| L16-8224 | HVAC grilles & registers at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 30 |

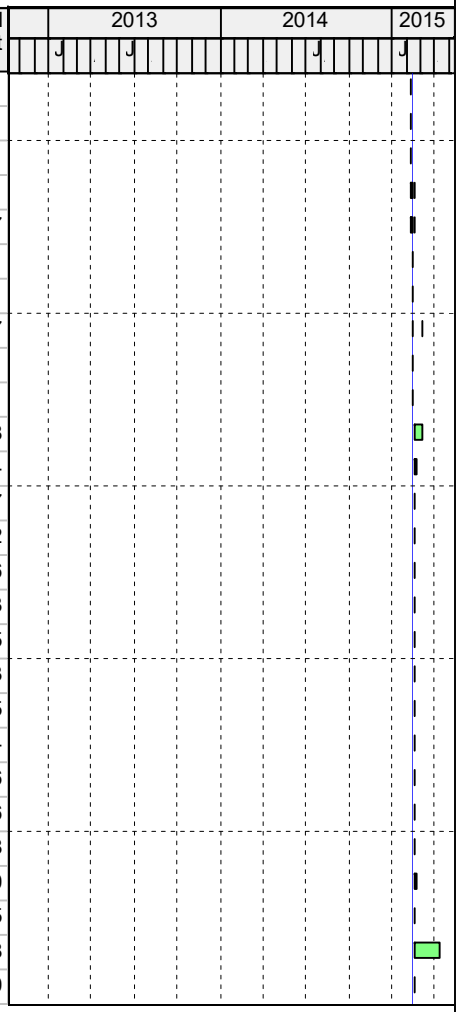



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8224 | HVAC grilles & registers at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 28 |
| L14-8224 | HVAC grilles & registers at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 26 |
| L12-8224 | HVAC grilles & registers at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 16 |
| L11-8224 | HVAC grilles & registers at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 14 |
| L10-8224 | HVAC grilles & registers at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 15 |
| L06-8224 | HVAC grilles & registers at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 16 |
| L05-8224 | HVAC grilles & registers at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 16 |
| L03-8224 | HVAC grilles & registers at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 23 |
| CO-7404 | Cx - FPT - Heat Pumps | 3 | 3 | 16-Feb-15 | 18-Feb-15 | 53 |
| SW-2040 | Zone 4 - Fine grade for sidewalk and planter curb | 3 | 3 | 16-Feb-15 | 18-Feb-15 | 22 |
| LL1-Z3-FCC28 | Electrical trim & finish at FCC | 4 | 4 | 16-Feb-15 | 19-Feb-15 | 16 |
| LL1-Z3-6036 | GWB hang, tape & finish ceiling at Food Prep (Dry St | 5 | 5 | 16-Feb-15 | 20-Feb-15 | 9 |
| L02-8148 | Paint at Locker Rooms | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 7 |
| LL1-6014Id2 | L1 bar redesign - install wall coverings at MR9 | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 12 |
| LL2-8146 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 16-Feb-15 | 18-Feb-15 | 26 |
| LL1-8172 | Ceiling grid & inspection at Exercise Room | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 8 |
| LL1-Z2-8144 | Install doors & hardware at corridors | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 27 |
| L1B-6011 | GWB, hang ceiling at West Ballrooms | 4 | 4 | 16-Feb-15 | 19-Feb-15 | 0 |
| L1B-8138 | GWB hang, tape & finish ceilings at corridors | 11 | 11 | 16-Feb-15 | 02-Mar-15 | 3 |
| L1L-8292 | GWB hang ceilings | 4 | 4 | 16-Feb-15 | 19-Feb-15 | 3 |
| MPT-1100 | Install spandrel, east (Elevation 44) | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 15 |
| I-5124 | Dining feature wall - install plywood backing | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 26 |
| L1BOH2-8104 | Paint, prime | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 10 |
| L17-7032 | Flooring - VCT (x42) | 1 | 1 | 17-Feb-15 | 17-Feb-15 | 26 |
| L16-7136 | Install doors & hardware | 1 | 1 | 17-Feb-15 | 17-Feb-15 | 55 |
| L17-7138 | Electrical trim & finish | 1 | 1 | 17-Feb-15 | 17-Feb-15 | 31 |
| L02-8130 | Ceiling grid at south half | 5 | 5 | 17-Feb-15 | 23-Feb-15 | 7 |

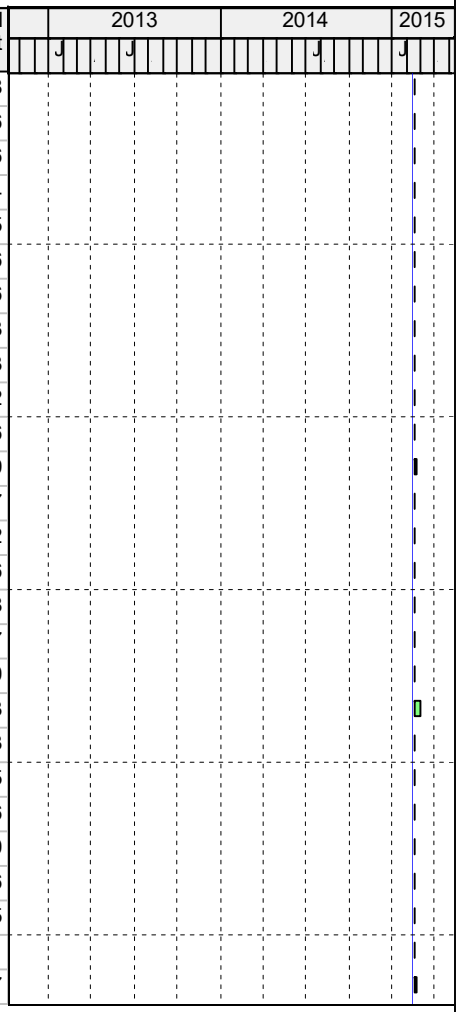



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8140 | Install window sills | 1 | 1 | 17-Feb-15 | 17-Feb-15 | 26 |
| L17-8224 | HVAC grilles & registers at corridors | 1 | 1 | 17-Feb-15 | 17-Feb-15 | 31 |
| LL1-Z3-8144 | Install toilets at Restrooms | 4 | 4 | 17-Feb-15 | 20-Feb-15 | 21 |
| SW-2044 | Zone 4 - FRP sidewalk | 3 | 3 | 17-Feb-15 | 19-Feb-15 | 22 |
| MPT-1092 | Caulking - Elevation 31 (above L12 terrace, west elev | 4 | 4 | 17-Feb-15 | 20-Feb-15 | 35 |
| MPT-1098 | Caulking - Elevation 30 (south elevation, west of man | 6 | 6 | 17-Feb-15 | 24-Feb-15 | 39 |
| L1K-8150 | HVAC drops/trim at ceiling | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 25 |
| LL1-8182 | Install doors & hardware at Exercise Room | 1 | 1 | 17-Feb-15 | 17-Feb-15 | 9 |
| L1K-8162 | Complete wallcoverings (FRP) | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 25 |
| LL4-8136 | Clear out and clean parking area | 10 | 10 | 17-Feb-15 | 02-Mar-15 | 22 |
| LL3-8136 | Clear out and clean parking area | 10 | 10 | 17-Feb-15 | 02-Mar-15 | 22 |
| MPT-1120 | Cap metal at L12 Terrace | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 38 |
| I-6012 | Core drill & install new floor drain and piping | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 2 |
| L03-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 18-Feb-15 | 18-Feb-15 | 26 |
| L03-7138 | Electrical trim & finish | 1 | 1 | 18-Feb-15 | 18-Feb-15 | 55 |
| L04-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 18-Feb-15 | 18-Feb-15 | 26 |
| L05-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 18-Feb-15 | 18-Feb-15 | 26 |
| CO-7258 | Cx - Start-Up - KMUA Trane (2) | 2 | 2 | 18-Feb-15 | 19-Feb-15 | 21 |
| EL-6044 | Elev 6 - Electrical trim & finish | 3 | 3 | 18-Feb-15 | 20-Feb-15 | 30 |
| EL-6046 | Elev 6 - Fire alarm trim | 3 | 3 | 18-Feb-15 | 20-Feb-15 | 30 |
| EL-6048 | Elev 6 - Fire sprinkler trim | 3 | 3 | 18-Feb-15 | 20-Feb-15 | 30 |
| EL-6050 | Elev 6 - Install pit grates | 3 | 3 | 18-Feb-15 | 20-Feb-15 | 30 |
| MPP-1020 | Elevation 18/19/21/22 & complete 45 (north elevatior | 7 | 7 | 18-Feb-15 | 25-Feb-15 | 15 |
| MPT-1062 | Elevation 32 metal panels (south elevation, east of m | 8 | 8 | 18-Feb-15 | 26-Feb-15 | 16 |
| CO-7139.1 | Install remaining devices & prep devices for testing - | 6 | 6 | 18-Feb-15 | 25-Feb-15 | 23 |
| L1K-8124a2 | Install doors & hardware | 2 | 2 | 18-Feb-15 | 19-Feb-15 | 5 |
| L1L-8276 | Paint, prime & first coat finish | 3 | 3 | 18-Feb-15 | 20-Feb-15 | 16 |

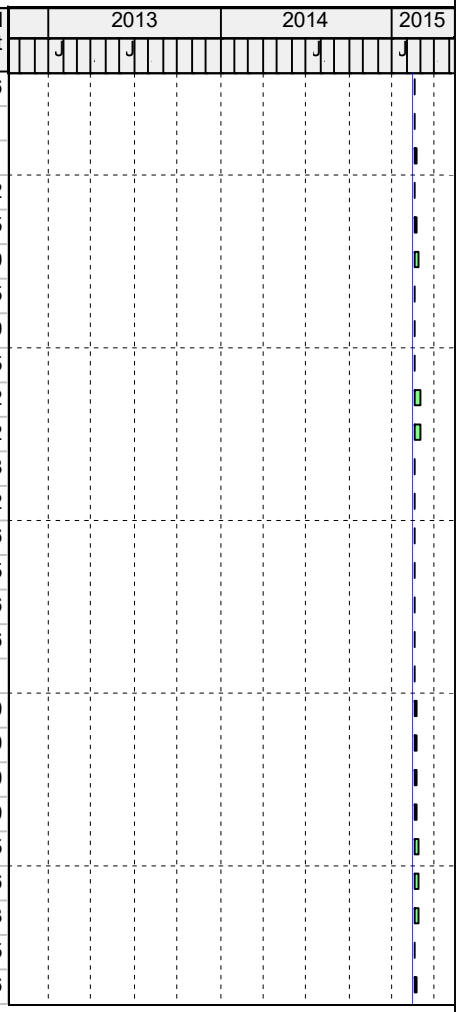



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-8174 | Wall coverings - vinyl at Exercise Room | 2 | 2 | 18-Feb-15 | 19-Feb-15 | 9 |
| LL1-8176 | HVAC drops/trim to grid | 1 | 1 | 18-Feb-15 | 18-Feb-15 | 8 |
| GB410-110 | Complete countertops - Levels 4-10 | 1 | 1 | 18-Feb-15 | 18-Feb-15 | 15 |
| GB410-112 | Complete shower/tub surrounds - Levels 4-10 | 1 | 1 | 18-Feb-15 | 18-Feb-15 | 15 |
| GB410-118 | Complete barn doors - Levels 4-10 | 1 | 1 | 18-Feb-15 | 18-Feb-15 | 20 |
| L1BOH2-8200 | Paint, first coat finish | 1 | 1 | 19-Feb-15 | 19-Feb-15 | 10 |
| CO-7110T | Fire Sprinkler Pre-Testing (Tower) - Tower Levels 4 thru | 6 | 6 | 19-Feb-15 | 26-Feb-15 | 16 |
| CO-7116T | Fire Alarm Pre-Testing (Tower) - Tower Levels 4 thru 1( | 6 | 6 | 19-Feb-15 | 26-Feb-15 | 16 |
| L06-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 19-Feb-15 | 19-Feb-15 | 26 |
| L07-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 19-Feb-15 | 19-Feb-15 | 26 |
| L08-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 19-Feb-15 | 19-Feb-15 | 26 |
| L1K-8148 | Lighting & electrical trim at ceiling | 2 | 2 | 19-Feb-15 | 20-Feb-15 | 25 |
| L1K-8125 | Floor prep | 2 | 2 | 19-Feb-15 | 20-Feb-15 | 25 |
| LL2-8148 | Fire sprinkler drops to grid | 1 | 1 | 19-Feb-15 | 19-Feb-15 | 26 |
| LL1-8178 | Lighting & electrical drops to grid | 2 | 2 | 19-Feb-15 | 20-Feb-15 | 8 |
| LL1-8180 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 19-Feb-15 | 20-Feb-15 | 8 |
| L1K-8164 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 19-Feb-15 | 20-Feb-15 | 25 |
| L02-8154 | Wall coverings - vinyl at north half | 3 | 3 | 19-Feb-15 | 23-Feb-15 | 3 |
| GB410-114 | Complete plumbing fixture installation - Levels 4-10 | 3 | 3 | 19-Feb-15 | 23-Feb-15 | 15 |
| CO-7140.1 | Fire Alarm System Device Testing - Tower Levels 3, 1' | 6 | 6 | 19-Feb-15 | 26-Feb-15 | 23 |
| L03-8669 | Install anchor bolts for trench drain | 1 | 1 | 19-Feb-15 | 19-Feb-15 | 2 |
| L1BOH2-8114 | Ceiling grid & inspection | 4 | 4 | 20-Feb-15 | 25-Feb-15 | 10 |
| L09-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 20-Feb-15 | 20-Feb-15 | 26 |
| L10-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 20-Feb-15 | 20-Feb-15 | 26 |
| L11-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 20-Feb-15 | 20-Feb-15 | 26 |
| CO-7220 | Cx - Start-Up - Common Space Heat Pump | 4 | 4 | 20-Feb-15 | 25-Feb-15 | 21 |
| CO-7222 | Cx - Start-Up - Kitchen Exhaust Fans | 2 | 2 | 20-Feb-15 | 23-Feb-15 | 23 |

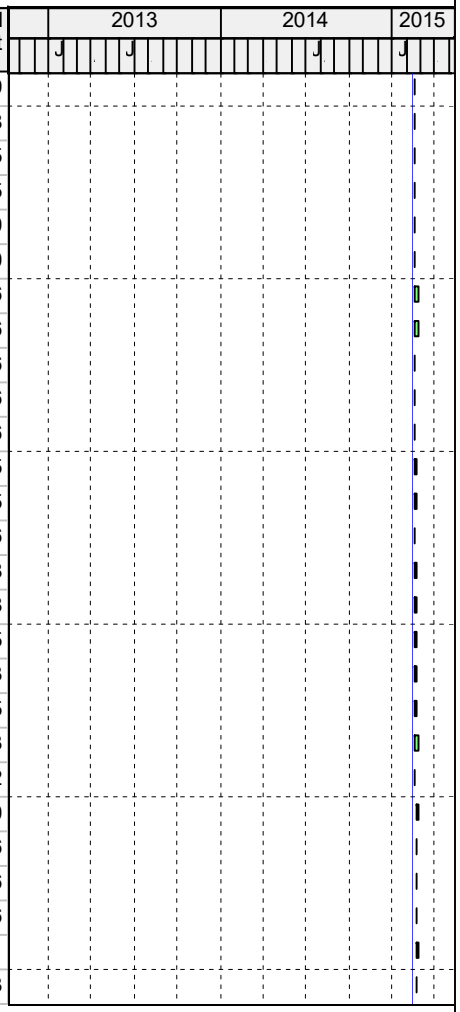



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7260 | Cx - Start-Up - Ballroom AAON RTU | 1 | 1 | 20-Feb-15 | 20-Feb-15 | 36 |
| CO-7262 | Cx - Start-Up - Electric Unit Heaters | 3 | 3 | 20-Feb-15 | 24-Feb-15 | 40 |
| LL1-Z3-FCC30 | Data/phone trim/finish at FCC | 4 | 4 | 20-Feb-15 | 25-Feb-15 | 16 |
| MPT-1038 | Install louvers, north | 3 | 3 | 20-Feb-15 | 23-Feb-15 | 38 |
| L1L-8258 | GWB tape & finish walls & ceilings | 7 | 7 | 20-Feb-15 | 02-Mar-15 | 3 |
| L1K-8123 | Floor prep | 1 | 1 | 20-Feb-15 | 20-Feb-15 | 5 |
| SW-2128 | Zone 1 - FRP planter wall at NE corner | 8 | 8 | 20-Feb-15 | 03-Mar-15 | 19 |
| LL1-8158 | Floor prep at corridors | 2 | 2 | 20-Feb-15 | 23-Feb-15 | 17 |
| L1B-6017 | GWB, hang ceiling at East Ballrooms | 4 | 4 | 20-Feb-15 | 25-Feb-15 | 0 |
| L1B-8102a | GWB, tape & finish ceiling at West Ballroom | 7 | 7 | 20-Feb-15 | 02-Mar-15 | 2 |
| MPT-1106 | Install alcoves, north | 3 | 3 | 20-Feb-15 | 23-Feb-15 | 46 |
| LL2-2106 | Floor prep | 1 | 1 | 20-Feb-15* | 20-Feb-15 | 3 |
| SW-2130 | Zone 1 - Waterproof wall | 2 | 2 | 20-Feb-15 | 23-Feb-15 | 33 |
| SW-2062 | Zone 4 - Patch curb & gutter | 2 | 2 | 20-Feb-15 | 23-Feb-15 | 27 |
| SW-2066 | Porte Cochere - FRP planter curb | 2 | 2 | 20-Feb-15 | 23-Feb-15 | 22 |
| LL1-Z2-8160a | Flooring - carpet at Meeting Rooms | 2 | 2 | 20-Feb-15 | 23-Feb-15 | 16 |
| L03-8684 | Pourback piping trench | 1 | 1 | 20-Feb-15 | 20-Feb-15 | 2 |
| L1K-8124a | Flooring - epoxy - east end | 4 | 4 | 21-Feb-15 | 25-Feb-15 | 6 |
| MPT-1102 | Elevation 32 spandrel panels (south elevation, east o | 2 | 2 | 21-Feb-15 | 23-Feb-15 | 62 |
| LL2-2104 | Flooring - epoxy at equipment alcoves | 5 | 5 | 21-Feb-15 | 26-Feb-15 | 4 |
| L03-8686 | Cure piping trench | 14 | 14 | 21-Feb-15 | 06-Mar-15 | 4 |
| L03-8408 | Install base at Elevator Lobby | 1 | 1 | 23-Feb-15 | 23-Feb-15 | 27 |
| L12-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 23-Feb-15 | 23-Feb-15 | 26 |
| L14-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 23-Feb-15 | 23-Feb-15 | 26 |
| L15-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 23-Feb-15 | 23-Feb-15 | 26 |
| SW-2212 | Zone 2 - FRP sidewalk panels | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 24 |
| CO-7264 | Cx - Start-Up - Lobby Trane TRU (2) | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 44 |

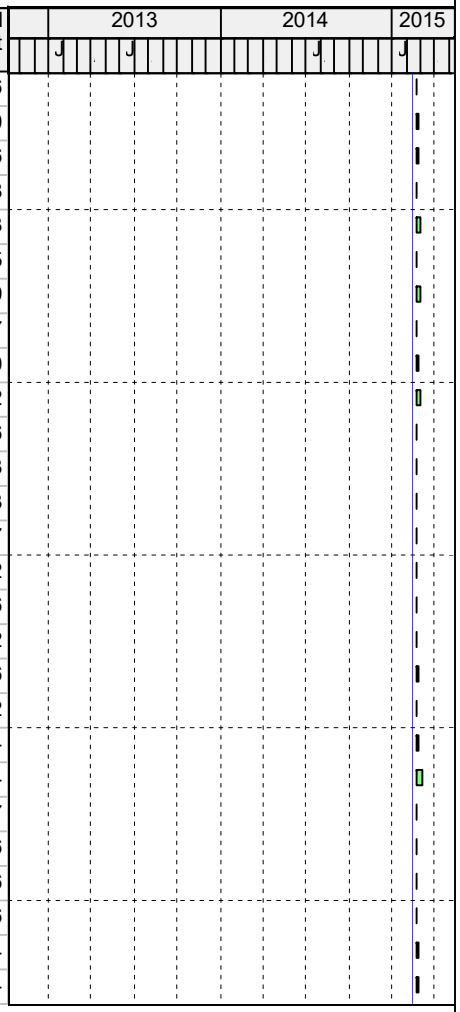



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7132 | Cx - DDC Point-To-Point - Ballroom VAV | 1 | 1 | 23-Feb-15 | 23-Feb-15 | 36 |
| MPT-1052 | Elevation 48/49 (north elevation, east of 51, L3-L17) | 3 | 3 | 23-Feb-15 | 25-Feb-15 | 41 |
| MPT-1084 | Caulking - Hi-roof cornice metal | 6 | 6 | 23-Feb-15 | 02-Mar-15 | 35 |
| LL1-8128 | Floor prep at Exercise Room | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 8 |
| LL1-8152 | Complete MEP trim | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 29 |
| L1K-8146 | Fire sprinkler drops/trim at ceiling | 1 | 1 | 23-Feb-15 | 23-Feb-15 | 26 |
| L1L-8230 | Paint, prime & first coat finish | 3 | 3 | 23-Feb-15 | 25-Feb-15 | 4 |
| SW-2222 | Zone 2 - Install j-box at NE corner | 1 | 1 | 23-Feb-15 | 23-Feb-15 | 24 |
| SW-2228 | Zone 2 - Pull wire and install light poles | 5 | 5 | 23-Feb-15 | 27-Feb-15 | 21 |
| SW-2232 | Zone 2 - Replace luminaire north of 3rd | 1 | 1 | 23-Feb-15 | 23-Feb-15 | 25 |
| SW-2328 | Zone 3 - Pull wire and install light poles | 5 | 5 | 23-Feb-15 | 27-Feb-15 | 26 |
| LL1-Z2-8142 | Wall coverings - vinyl at corridors | 3 | 3 | 23-Feb-15 | 25-Feb-15 | 21 |
| L1L-8142 | HVAC drops to 9-wood ceiling - north of Grid K | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 5 |
| L1L-8144 | Electrical drops to 9-wood ceiling - north of Grid K | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 5 |
| L1L-8146 | Fire sprinkler drops to 9-wood ceiling - north of Grid K | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 5 |
| LL1-Z3-8156 | Install countertops at restrooms | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 23 |
| LL1-Z3-8158 | Install toilet partitions | 4 | 4 | 23-Feb-15 | 26-Feb-15 | 21 |
| MPT-1110 | Cap metal at hi-roof | 5 | 5 | 23-Feb-15 | 27-Feb-15 | 36 |
| L1L-8114a | Install 9-wood celing supports - south of Grid K | 3 | 3 | 23-Feb-15 | 25-Feb-15 | 7 |
| L1L-8108 | GWB hang walls & ceilings (Bar) | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 1 |
| L16-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 24-Feb-15 | 24-Feb-15 | 26 |
| L17-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 24-Feb-15 | 24-Feb-15 | 26 |
| CO-7256 | Cx - Start-Up - Elevator Machine Room Ductless Split | 1 | 1 | 24-Feb-15 | 24-Feb-15 | 23 |
| CO-7134 | Cx - DDC Point-To-Point - Ballroom RTU (2) | 2 | 2 | 24-Feb-15 | 25-Feb-15 | 36 |
| MPP-1048 | Caulking - Porte Cochere cornice metal | 3 | 3 | 24-Feb-15 | 26-Feb-15 | 37 |
| L02-8142 | Ceiling grid at Locker Rooms | 4 | 4 | 24-Feb-15 | 27-Feb-15 | 3 |
| LL1-8162 | Flooring - carpet at corridors | 5 | 5 | 24-Feb-15 | 02-Mar-15 | 17 |

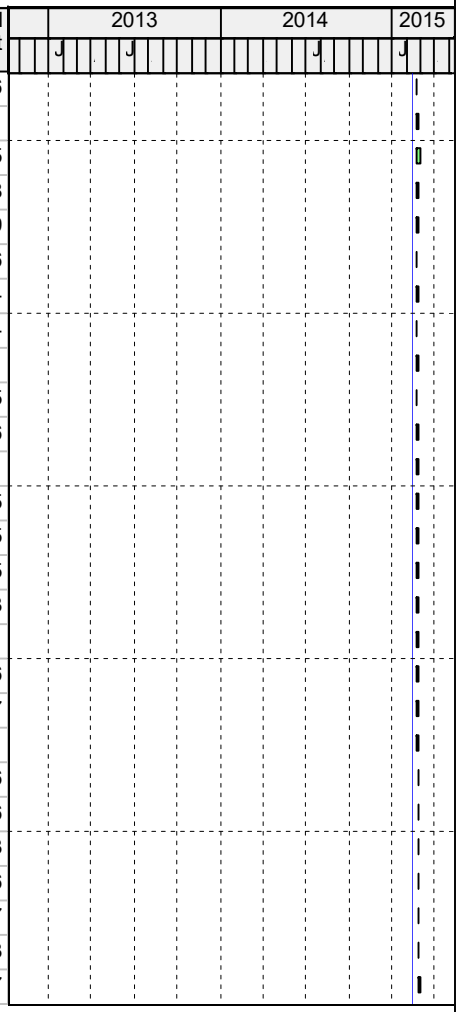



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8156 | Install doors & hardware at north half | 3 | 3 | 24-Feb-15 | 26-Feb-15 | 16 |
| L02-8158 | Ceiling grid at north half | 3 | 3 | 24-Feb-15 | 26-Feb-15 | 3 |
| GB410-116 | Complete shower doors - Levels 4-10 | 2 | 2 | 24-Feb-15 | 25-Feb-15 | 15 |
| MPP-1060 | Install alcoves, south | 2 | 2 | 24-Feb-15 | 25-Feb-15 | 46 |
| SW-2064 | Porte Cochere - Fill and grade Porte Cochere drive | 3 | 3 | 24-Feb-15 | 26-Feb-15 | 22 |
| MPT-1118 | Cap metal - Pool terrace | 3 | 3 | 24-Feb-15 | 26-Feb-15 | 37 |
| LL1-Z2-8118a | Install decorative light fixtures | 3 | 3 | 25-Feb-15 | 27-Feb-15 | 16 |
| CO-7226 | Cx - Start-Up - Misc. Equipment | 5 | 5 | 25-Feb-15 | 03-Mar-15 | 40 |
| CO-7228 | Cx - Start-Up - Poolpak | 1 | 1 | 25-Feb-15 | 25-Feb-15 | 44 |
| MPP-1036 | Podium Signs, East | 5 | 5 | 25-Feb-15 | 03-Mar-15 | 29 |
| LL1-8130 | Install base | 3 | 3 | 25-Feb-15 | 27-Feb-15 | 16 |
| LL1-8136 | Ceramic tile in restrooms | 3 | 3 | 25-Feb-15 | 27-Feb-15 | 8 |
| L1K-8202 | Ceiling grid at Janitorial | 1 | 1 | 25-Feb-15 | 25-Feb-15 | 1 |
| LL1-Z2-8122 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 25-Feb-15 | 27-Feb-15 | 16 |
| LL1-Z2-8136 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 25-Feb-15 | 27-Feb-15 | 19 |
| GB1117-102 | Complete painting - Levels 3, 11-17 | 3 | 3 | 25-Feb-15 | 27-Feb-15 | 14 |
| L1L-8110 | GWB tape & finish walls & ceilings (Bar) | 7 | 7 | 25-Feb-15 | 05-Mar-15 | 1 |
| LL1-Z3-8162 | Install sinks at Restrooms | 2 | 2 | 25-Feb-15 | 26-Feb-15 | 23 |
| L1BOH2-8126 | Install doors & hardware | 3 | 3 | 26-Feb-15 | 02-Mar-15 | 10 |
| L1BOH2-8204 | HVAC drops/trim at ceiling | 2 | 2 | 26-Feb-15 | 27-Feb-15 | 14 |
| RF-4070 | TR - Terrace Roof - Install American Hydrotech assem | 3 | 3 | 26-Feb-15 | 02-Mar-15 | 35 |
| CO-7224 | Cx - Start-Up - Gravity Relief Ventilator | 1 | 1 | 26-Feb-15 | 26-Feb-15 | 21 |
| CO-7136 | Cx - DDC Point-To-Point - MUA AAON Start-Up (8) | 5 | 5 | 26-Feb-15 | 04-Mar-15 | 36 |
| SW-2042 | Porte Cochere - Install trench drain | 3 | 3 | 26-Feb-15 | 02-Mar-15 | 22 |
| LL1-Z3-FCC32 | Flooring - VCT at FCC | 3 | 3 | 26-Feb-15 | 02-Mar-15 | 16 |
| MPT-1082 | Caulking - Elevation 48/49 (north elevation, east of 5 | 4 | 4 | 26-Feb-15 | 03-Mar-15 | 34 |
| L02-8140 | Lighting & electrical trim at south half | 3 | 3 | 26-Feb-15 | 02-Mar-15 | 7 |

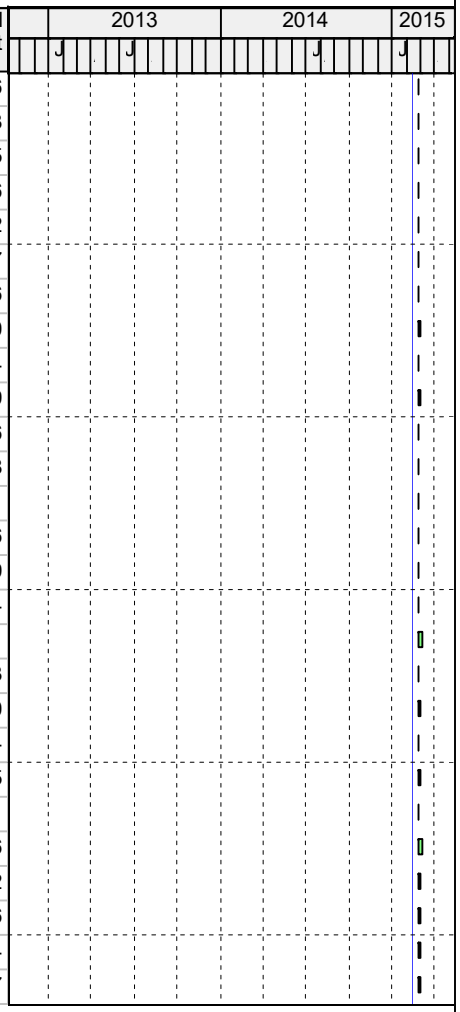



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8232 | Wall coverings - vinyl | 5 | 5 | 26-Feb-15 | 04-Mar-15 | 23 |
| I-3102 | GWB, tape & finish ceiling at East Ballroom | 7 | 7 | 26-Feb-15 | 06-Mar-15 | 0 |
| MPP-1064 | Install column at Pool | 1 | 1 | 26-Feb-15 | 26-Feb-15 | 15 |
| L1L-8310 | Install 9-wood ceiling supports at Sitting Area | 2 | 2 | 26-Feb-15 | 27-Feb-15 | 4 |
| L1L-8142a | HVAC drops to 9-wood ceiling - south of Grid K | 2 | 2 | 26-Feb-15 | 27-Feb-15 | 7 |
| L1L-8144a | Electrical drops to 9-wood ceiling - south of Grid K | 2 | 2 | 26-Feb-15 | 27-Feb-15 | 7 |
| L1L-8146a | Fire sprinkler drops to 9-wood ceiling - south of Grid K | 2 | 2 | 26-Feb-15 | 27-Feb-15 | 7 |
| L1K-8124b | Flooring - epoxy - west end | 7 | 7 | 26-Feb-15 | 06-Mar-15 | 5 |
| LL2-2048 | Set Laundry Room equipment (BY OTHERS) | 1 | 1 | 27-Feb-15 | 27-Feb-15 | 3 |
| MPP-1004 | Pool Area cornice metal | 8 | 8 | 27-Feb-15 | 07-Mar-15 | 15 |
| CO-7104T | Fire Alarm & Smoke Control Pre-Testing (Tower) - Tow | 7 | 7 | 27-Feb-15 | 09-Mar-15 | 16 |
| LL1-Z2-8124a | Install base | 10 | 10 | 27-Feb-15 | 12-Mar-15 | 15 |
| MPT-1060 | Elevation 33/34 hat channel (east elevation, south er | 3 | 3 | 27-Feb-15 | 02-Mar-15 | 16 |
| MPT-1094 | Caulking - Elevation 32 (south elevation, east of man | 10 | 10 | 27-Feb-15 | 12-Mar-15 | 22 |
| L1K-8212 | Lighting & electrical trim at ceiling | 2 | 2 | 27-Feb-15 | 02-Mar-15 | 1 |
| L02-8160 | HVAC drops/trim at north half | 2 | 2 | 27-Feb-15 | 02-Mar-15 | 9 |
| LL1-Z3-8160 | Install doors & hardware at restrooms | 2 | 2 | 27-Feb-15 | 02-Mar-15 | 21 |
| LL2-2050 | Laundry Room equipment final connections (MEP) | 3 | 3 | 02-Mar-15 | 04-Mar-15 | 3 |
| L03-8622 | HVAC trim at Pool | 2 | 2 | 02-Mar-15 | 03-Mar-15 | 11 |
| L1BOH2C-6024 | Lighting & electrical trim at ceiling | 2 | 2 | 02-Mar-15 | 03-Mar-15 | 14 |
| L02-8145 | MEP drops to framed ceiling (including inspections) | 4 | 4 | 02-Mar-15 | 05-Mar-15 | 3 |
| LL1-8138 | Flooring - install cork floor at Exercise Room | 3 | 3 | 02-Mar-15 | 04-Mar-15 | 16 |
| LL1-Z2-8123 | Floor prep | 2 | 2 | 02-Mar-15 | 03-Mar-15 | 16 |
| SW-2056 | Zone 4 - Pull wire and replace luminaires on 110th | 5 | 5 | 02-Mar-15 | 06-Mar-15 | 29 |
| LL1-Z2-8128 | HVAC trim at ceiling | 1 | 1 | 02-Mar-15 | 02-Mar-15 | 16 |
| LL1-Z2-8146 | Floor prep at corridors | 2 | 2 | 02-Mar-15 | 03-Mar-15 | 19 |
| L1BOH2C-6026 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 02-Mar-15 | 03-Mar-15 | 14 |

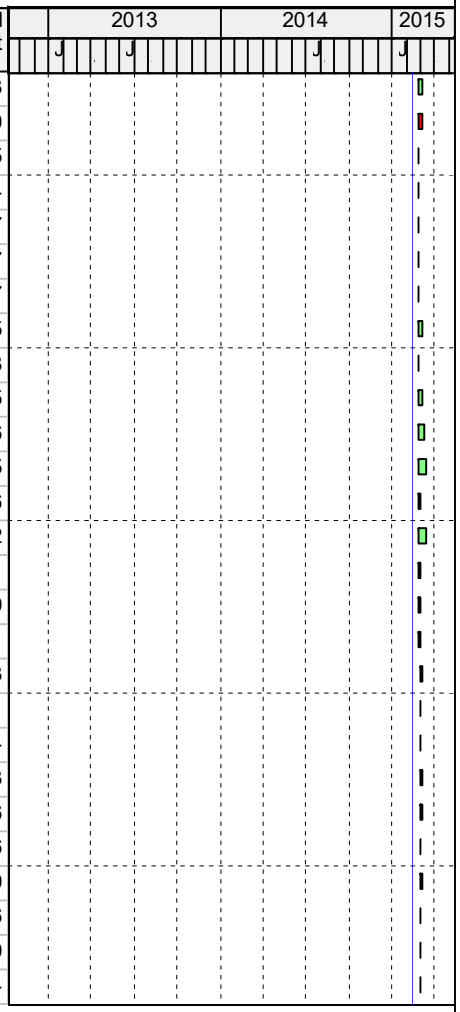



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| GB1117-104 | Complete vinyl wallcoverings - Levels 3, 11-17 | 5 | 5 | 02-Mar-15 | 06-Mar-15 | 14 |
| GB1117-106 | Complete flooring - Levels 3, 11-17 | 4 | 4 | 02-Mar-15 | 05-Mar-15 | 15 |
| L1L-8312 | HVAC drops to 9-wood ceiling | 2 | 2 | 02-Mar-15 | 03-Mar-15 | 4 |
| L1L-8314 | Electrical drops to 9-wood ceiling | 2 | 2 | 02-Mar-15 | 03-Mar-15 | 4 |
| L1L-8316 | Fire sprinkler drops to 9-wood ceiling | 2 | 2 | 02-Mar-15 | 03-Mar-15 | 4 |
| CM-1024 | Tower - "Clean/Punch" Complete - All Floors | 0 | 0 | | 02-Mar-15 | 13 |
| L1BOH2-8116 | Finish carpentry/millwork | 5 | 5 | 03-Mar-15 | 09-Mar-15 | 10 |
| LL1-Z3-8146 | Install restroom accessories | 2 | 2 | 03-Mar-15 | 04-Mar-15 | 21 |
| SW-2048 | Porte Cochere - FRP Porte Cochere drive | 5 | 5 | 03-Mar-15 | 09-Mar-15 | 22 |
| LL1-Z3-FCC34 | Paint, final coat & touch-up up at FCC | 2 | 2 | 03-Mar-15 | 04-Mar-15 | 16 |
| LL1-Z3-FCC36 | Install doors & hardware at FCC | 2 | 2 | 03-Mar-15 | 04-Mar-15 | 16 |
| MPT-1064 | Elevation 33/34 metal panels (east elevation, south e | 8 | 8 | 03-Mar-15 | 11-Mar-15 | 16 |
| L1BOH2-8120 | Wall coverings - vinyl | 3 | 3 | 03-Mar-15 | 05-Mar-15 | 12 |
| I-1208 | Paint, prime & first coat finish | 2 | 2 | 03-Mar-15 | 04-Mar-15 | 3 |
| LL1-8166 | Install base at corridors | 5 | 5 | 03-Mar-15 | 09-Mar-15 | 17 |
| LL1-Z2-8130 | Fire sprinkler trim | 1 | 1 | 03-Mar-15 | 03-Mar-15 | 16 |
| L1K-8218 | Floor prep | 2 | 2 | 03-Mar-15 | 04-Mar-15 | 1 |
| L1B-6019 | Install clouds at West Ballrooms | 7 | 7 | 03-Mar-15 | 11-Mar-15 | 2 |
| L1B-8142 | Paint, prime & first coat finish walls & ceilings at corrid | 2 | 2 | 03-Mar-15 | 04-Mar-15 | 3 |
| L02-8114 | Floor prep at south half | 2 | 2 | 03-Mar-15 | 04-Mar-15 | 7 |
| L02-8162 | Lighting & electrical trim at north half | 3 | 3 | 03-Mar-15 | 05-Mar-15 | 9 |
| L02-8164 | Fire alarm trim (speaker/strobe & smoke detector bas | 3 | 3 | 03-Mar-15 | 05-Mar-15 | 9 |
| LL4-8138 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 7 | 03-Mar-15 | 11-Mar-15 | 22 |
| LL3-8138 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 7 | 03-Mar-15 | 11-Mar-15 | 22 |
| L1BOH2-8112 | Fire sprinkler drops/trim at ceiling | 1 | 1 | 04-Mar-15 | 04-Mar-15 | 15 |
| SW-2218 | Zone 2 - Install landscaping & irrigation | 5 | 5 | 04-Mar-15 | 10-Mar-15 | 19 |
| CO-7230 | Cx - TAB - Air Balancing | 15 | 15 | 04-Mar-15 | 24-Mar-15 | 18 |

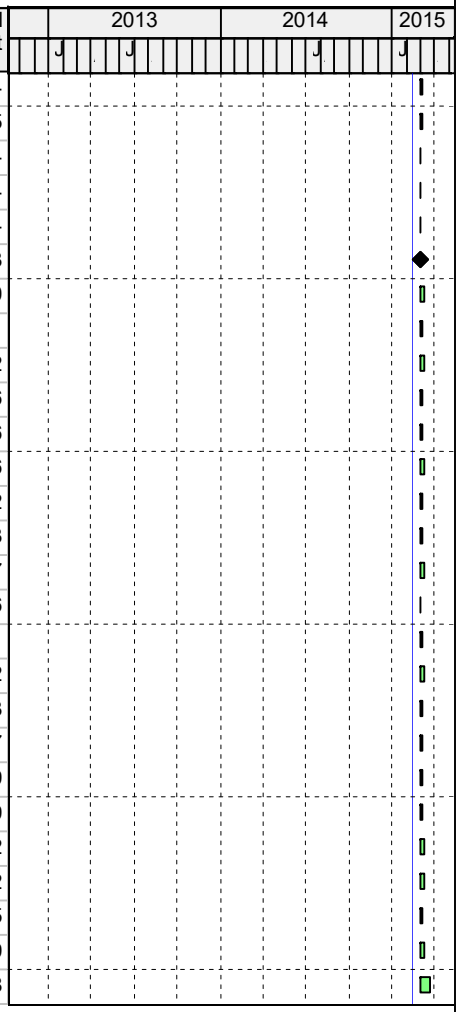



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8666 | Electrical trim & finish at ceiling at Pool | 2 | 2 | 04-Mar-15 | 05-Mar-15 | 11 |
| LL1-Z3-6038 | Paint ceiling at Food Prep (Dry Storage) | 2 | 2 | 04-Mar-15 | 05-Mar-15 | 9 |
| L1L-8318 | Install 9-wood ceiling at Sitting Area | 3 | 3 | 04-Mar-15 | 06-Mar-15 | 4 |
| LL2-2086 | Flooring - epoxy remainder of floor | 5 | 5 | 05-Mar-15 | 11-Mar-15 | 3 |
| L1K-8210 | Ceramic tile in restrooms | 7 | 7 | 05-Mar-15 | 13-Mar-15 | 1 |
| CO-7402 | Cx - FPT - Central Plant | 2 | 2 | 05-Mar-15 | 06-Mar-15 | 36 |
| I-1206 | Install ceiling at Concierge Lounge | 10 | 10 | 05-Mar-15 | 18-Mar-15 | 3 |
| LL1-Z3-FCC38 | Final clean and punch list at FCC | 3 | 3 | 05-Mar-15 | 09-Mar-15 | 16 |
| LL1-8142 | Plumbing fixtures & trim | 2 | 2 | 05-Mar-15 | 06-Mar-15 | 19 |
| LL1-8144 | Finish carpentry/millwork | 5 | 5 | 05-Mar-15 | 11-Mar-15 | 16 |
| L1L-8260 | Wall coverings - vinyl | 3 | 3 | 05-Mar-15 | 09-Mar-15 | 12 |
| LL1-Z3-8150 | Paint, final coat & touch-up | 2 | 2 | 05-Mar-15 | 06-Mar-15 | 21 |
| LL1-Z3-8154 | Complete MEP trim at Restroom | 2 | 2 | 05-Mar-15 | 06-Mar-15 | 21 |
| L1B-8162 | Install doors & hardware at corridors | 2 | 2 | 05-Mar-15 | 06-Mar-15 | 16 |
| L02-8152 | Flooring - VCT at south half | 2 | 2 | 05-Mar-15 | 06-Mar-15 | 7 |
| L03-8624 | Fire sprinkler trim at Pool | 2 | 2 | 06-Mar-15 | 09-Mar-15 | 11 |
| L02-8150 | Install doors & hardware at Locker Rooms | 1 | 1 | 06-Mar-15 | 06-Mar-15 | 3 |
| LL1-Z2-8160 | Flooring - carpet at Jr. Ballroom | 3 | 3 | 06-Mar-15 | 10-Mar-15 | 14 |
| LL1-Z3-8120 | Wall coverings - vinyl | 4 | 4 | 06-Mar-15 | 11-Mar-15 | 9 |
| L1BOH2-8123 | Floor prep | 2 | 2 | 06-Mar-15 | 09-Mar-15 | 12 |
| L02-8166 | Fire sprinkler trim at north half | 2 | 2 | 06-Mar-15 | 09-Mar-15 | 9 |
| L02-8168 | Floor prep at north half | 2 | 2 | 06-Mar-15 | 09-Mar-15 | 9 |
| L1L-8140a | Install 9-wood ceiling - south of Grid K | 5 | 5 | 06-Mar-15 | 12-Mar-15 | 3 |
| L1L-8154 | Paint, prime & first finish coat (Bar) | 2 | 2 | 06-Mar-15 | 09-Mar-15 | 1 |
| L1K-8128 | Install Kitchen equipment (BY OTHERS) | 5 | 5 | 09-Mar-15 | 13-Mar-15 | 5 |
| CO-7408 | Cx - FPT - Garage Exhaust Fans | 1 | 1 | 09-Mar-15 | 09-Mar-15 | 36 |
| MPP-1040 | Caulking - Pool Area & Ballroom cornice metal | 8 | 8 | 09-Mar-15 | 18-Mar-15 | 13 |

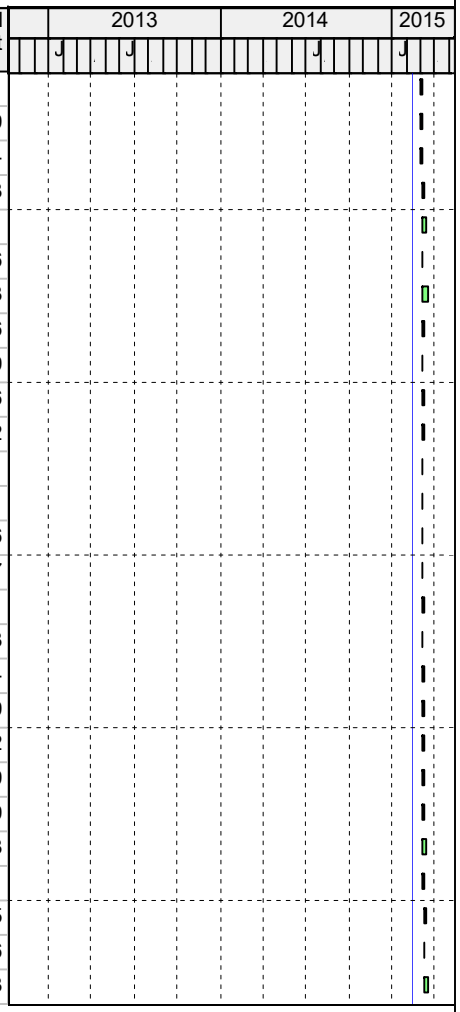



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-8150 | Install bathroom accessories | 2 | 2 | 09-Mar-15 | 10-Mar-15 | 19 |
| L1L-8238 | HVAC drops/trim at celing | 2 | 2 | 09-Mar-15 | 10-Mar-15 | 15 |
| L1L-8239 | Floor prep | 2 | 2 | 09-Mar-15 | 10-Mar-15 | 4 |
| L1B-6037 | Install clouds at East Ballroom | 7 | 7 | 09-Mar-15 | 17-Mar-15 | 0 |
| L1L-8206 | Lighting & electrical trim at ceilings - north of Grid K | 2 | 2 | 09-Mar-15 | 10-Mar-15 | 11 |
| L1L-8308 | Floor (stair) prep | 1 | 1 | 09-Mar-15 | 09-Mar-15 | 5 |
| GB1117-108 | Complete base - Levels 3, 11-17 | 5 | 5 | 09-Mar-15 | 13-Mar-15 | 16 |
| GB1117-110 | Complete countertops - Levels 3, 11-17 | 1 | 1 | 09-Mar-15 | 09-Mar-15 | 16 |
| GB1117-112 | Complete shower/tub surrounds - Levels 3, 11-17 | 3 | 3 | 09-Mar-15 | 11-Mar-15 | 14 |
| CO-7144 | Final Inspection - Transportation (Right-Of-Way) | 5 | 5 | 09-Mar-15 | 13-Mar-15 | 36 |
| CO-7148 | Final Inspection - Utilities | 5 | 5 | 09-Mar-15 | 13-Mar-15 | 36 |
| L03-8682 | Install waterproofing and protection layer | 3 | 3 | 09-Mar-15 | 11-Mar-15 | 2 |
| L1BOH2-8124 | Flooring - VCT | 3 | 3 | 10-Mar-15 | 12-Mar-15 | 12 |
| L1BOH2-8124a | Install base | 5 | 5 | 10-Mar-15 | 16-Mar-15 | 10 |
| CO-7410 | Cx - FPT - Misc Equipment | 4 | 4 | 10-Mar-15 | 13-Mar-15 | 36 |
| LL1-Z3-FCC40 | Install Knox Box at FCC | 2 | 2 | 10-Mar-15 | 11-Mar-15 | 16 |
| CO-7110T.1 | Fire Sprinkler Pre-Testing (Tower) - Tower Levels 3, 11 | 6 | 6 | 10-Mar-15 | 17-Mar-15 | 16 |
| O-7116T.1 | Fire Alarm Pre-Testing (Tower) - Tower Levels 3, 11 thr | 6 | 6 | 10-Mar-15 | 17-Mar-15 | 16 |
| L1L-8128 | Install die wall (Bar) | 3 | 3 | 10-Mar-15 | 12-Mar-15 | 1 |
| L1L-8280 | Install Peter Glassford art wall | 5 | 5 | 10-Mar-15 | 16-Mar-15 | 5 |
| L1L-8123 | Floor prep - north of Grid K | 2 | 2 | 10-Mar-15 | 11-Mar-15 | 11 |
| LL1-8164 | Complete MEP trim at corridors | 2 | 2 | 10-Mar-15 | 11-Mar-15 | 18 |
| LL1-8168 | Paint, final coat & touch-up | 2 | 2 | 10-Mar-15 | 11-Mar-15 | 18 |
| LL1-Z3-8206 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 10-Mar-15 | 12-Mar-15 | 12 |
| L02-8170 | Flooring - VCT at north half | 3 | 3 | 10-Mar-15 | 12-Mar-15 | 9 |
| MPP-1050 | Columns at Porte Cochere | 4 | 4 | 10-Mar-15 | 13-Mar-15 | 26 |
| L1L-8236 | Lighting & electrical trim at ceilings | 3 | 3 | 11-Mar-15 | 13-Mar-15 | 15 |

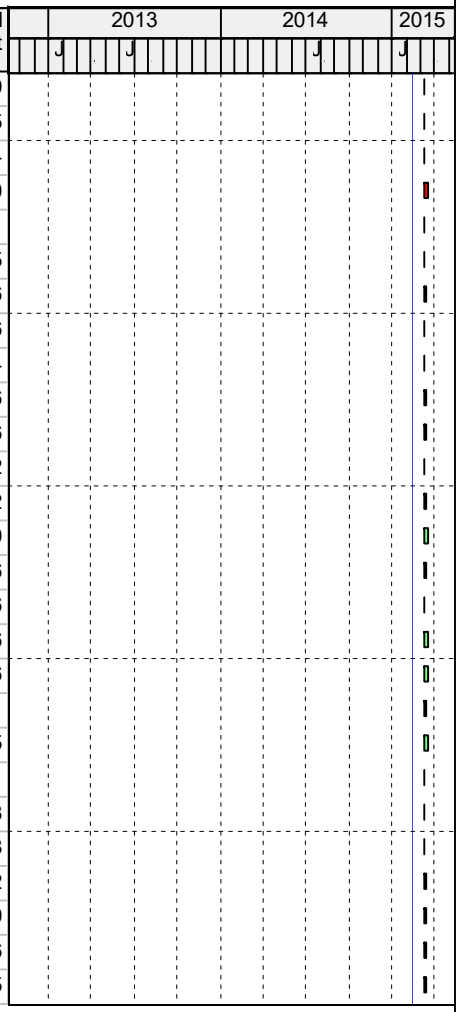



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8242 | Finish carpentry/millwork (including front desk) | 15 | 15 | 11-Mar-15 | 31-Mar-15 | 4 |
| SW-2330 | Zone 3 - Landscaping & irrigation | 5 | 5 | 11-Mar-15 | 17-Mar-15 | 19 |
| LL1-Z2-8148 | Flooring - carpet at corridors | 3 | 3 | 11-Mar-15 | 13-Mar-15 | 14 |
| LL1-Z2-8150 | Install base at corridors | 3 | 3 | 11-Mar-15 | 13-Mar-15 | 14 |
| L1B-8144 | Wall coverings - vinyl at corridors | 3 | 3 | 11-Mar-15 | 13-Mar-15 | 11 |
| L1B-8146 | HVAC drops/trim at corridors | 2 | 2 | 11-Mar-15 | 12-Mar-15 | 3 |
| L1L-8286 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 11-Mar-15 | 13-Mar-15 | 15 |
| L1L-8302 | Lighting & electrical trim at ceilings | 3 | 3 | 11-Mar-15 | 13-Mar-15 | 18 |
| L1L-8304 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 11-Mar-15 | 13-Mar-15 | 18 |
| L03-8644 | Connect, startup & adjust pool equipment | 10 | 10 | 12-Mar-15 | 25-Mar-15 | 4 |
| LL2-2062 | Ceiling grid at Laundry | 4 | 4 | 12-Mar-15 | 17-Mar-15 | 3 |
| LL1-Z3-FCC22 | Final inspections by CoB and Fire Marshall | 2 | 2 | 12-Mar-15 | 13-Mar-15 | 16 |
| L03-8670 | Installl trench drains at Pool | 2 | 2 | 12-Mar-15 | 13-Mar-15 | 2 |
| MPT-1096 | Caulking - Elevation 33/34 (east elevation, south end | 10 | 10 | 12-Mar-15 | 25-Mar-15 | 13 |
| LL1-8146 | Complete MEP trim | 2 | 2 | 12-Mar-15 | 13-Mar-15 | 16 |
| LL1-8148 | Acoustical ceiling tile | 2 | 2 | 12-Mar-15 | 13-Mar-15 | 16 |
| L1L-8266 | HVAC drops/trim at celing | 2 | 2 | 12-Mar-15 | 13-Mar-15 | 4 |
| LL1-8188 | Paint, final coat & touch-up | 2 | 2 | 12-Mar-15 | 13-Mar-15 | 16 |
| LL1-Z3-8128 | Flooring - VCT | 3 | 3 | 12-Mar-15 | 16-Mar-15 | 9 |
| GB1117-114 | Complete plumbing fixture installation - Levels 3, 11-1 | 4 | 4 | 12-Mar-15 | 17-Mar-15 | 14 |
| LL1-Z2-8152 | Complete MEP trim | 2 | 2 | 13-Mar-15 | 16-Mar-15 | 15 |
| L1B-8148 | Lighting & electrical trim at corridors | 2 | 2 | 13-Mar-15 | 16-Mar-15 | 3 |
| L1B-8150 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 13-Mar-15 | 16-Mar-15 | 9 |
| L02-8172 | Finish carpentry/millwork at north half | 3 | 3 | 13-Mar-15 | 17-Mar-15 | 9 |
| L1L-8148 | Electrical rough-in at die wall (Bar) | 5 | 5 | 13-Mar-15 | 19-Mar-15 | 1 |
| L1L-8150 | Plumbing rough-in at die wall (Bar) | 5 | 5 | 13-Mar-15 | 19-Mar-15 | 1 |
| L1L-8204a | HVAC trim at ceiling - south of Grid K | 1 | 1 | 13-Mar-15 | 13-Mar-15 | 3 |

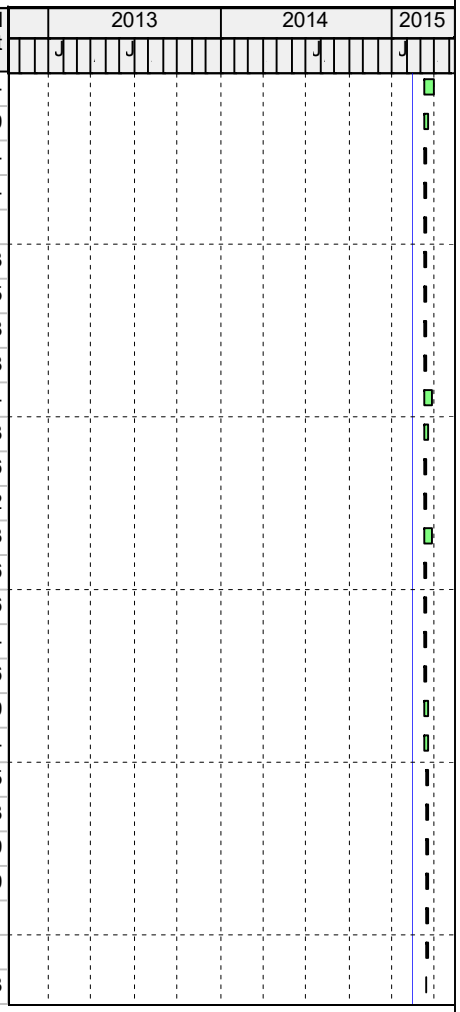



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPP-1018 | Elevation A/B/C (Porte Cochere wall panels) | 2 | 2 | 14-Mar-15 | 16-Mar-15 | 26 |
| L1K-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 14 |
| L1K-8206 | Install toilets at restrooms | 4 | 4 | 16-Mar-15 | 19-Mar-15 | 1 |
| L1K-8128a | Kitchen Equipment Final Connections | 5 | 5 | 16-Mar-15 | 20-Mar-15 | 5 |
| L1L-8234 | Fire sprinkler trim at ceilings | 1 | 1 | 16-Mar-15 | 16-Mar-15 | 15 |
| L1L-8264 | Lighting & electrical trim at ceilings | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 4 |
| LL1-Z2-8154 | Complete MEP trim in corridors | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 14 |
| LL1-Z2-8156 | Paint, final coat & touch-up | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 14 |
| L1L-8298 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 5 |
| L1L-8306 | Fire sprinkler trim | 1 | 1 | 16-Mar-15 | 16-Mar-15 | 18 |
| GB1117-118 | Complete barn doors - Levels 3, 11-17 | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 16 |
| LL2-8152 | Clear out and clean parking area | 10 | 10 | 16-Mar-15* | 27-Mar-15 | 11 |
| L1L-8206a | Lighting & elecrical trim at ceilings - south of Grid K | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 3 |
| L1K-8128b | Ansul system final connections | 5 | 5 | 16-Mar-15 | 20-Mar-15 | 5 |
| LL1-8190 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 16-Mar-15 | 20-Mar-15 | 16 |
| LL2-8156 | Remove job shacks | 1 | 1 | 16-Mar-15 | 16-Mar-15 | 22 |
| L1BOH2-8128 | Flooring - carpet | 3 | 3 | 17-Mar-15 | 19-Mar-15 | 10 |
| L1L-8278 | Flooring - tile at stair treads | 10 | 10 | 17-Mar-15 | 30-Mar-15 | 5 |
| L1B-8152 | Fire sprinkler drops/trim at corridors | 1 | 1 | 17-Mar-15 | 17-Mar-15 | 9 |
| L1B-8160 | Floor prep | 2 | 2 | 17-Mar-15 | 18-Mar-15 | 3 |
| MPP-1056 | Caulking - Porte Cochere walls & columns | 3 | 3 | 17-Mar-15 | 19-Mar-15 | 22 |
| L1B-8206 | Ceiling grid at West Ballrooms | 4 | 4 | 17-Mar-15 | 20-Mar-15 | 2 |
| L1L-8123a | Floor prep - south of Grid K | 2 | 2 | 17-Mar-15 | 18-Mar-15 | 3 |
| SW-2122 | Zone 1 - Install landscaping & irrigation | 3 | 3 | 18-Mar-15 | 20-Mar-15 | 19 |
| CO-7138 | Elevator Finals with AHJ | 5 | 5 | 18-Mar-15 | 24-Mar-15 | 18 |
| CO-7104T.1 | Fire Alarm & Smoke Control Pre-Testing (Tower) - Tow | 7 | 7 | 18-Mar-15 | 26-Mar-15 | 16 |
| L1L-8262 | Fire sprinkler trim at ceilings | 1 | 1 | 18-Mar-15 | 18-Mar-15 | 5 |

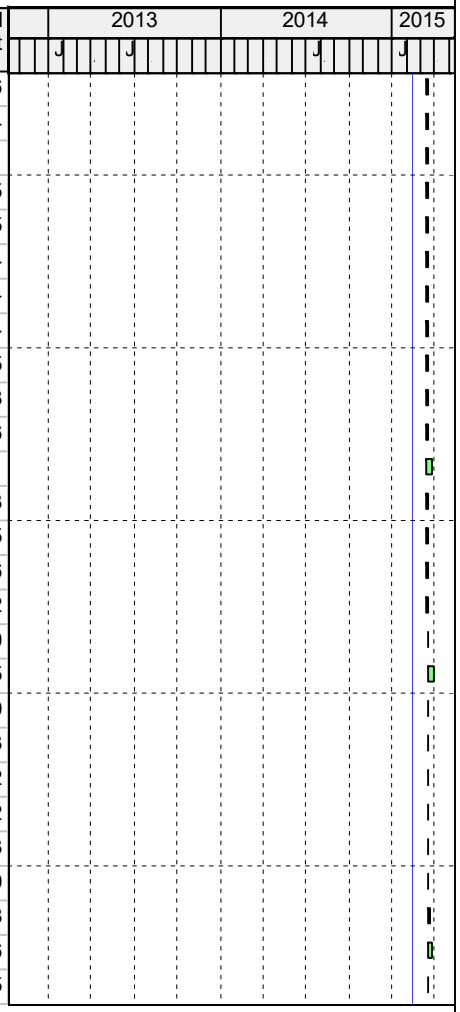



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2098 | HVAC drops to grid at Laundry | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 3 |
| GB1117-116 | Complete shower doors - Levels 3, 11-17 | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 14 |
| L1L-8112a | Fire sprinkler trim - south of Grid K | 1 | 1 | 18-Mar-15 | 18-Mar-15 | 3 |
| L1L-8118a | Fire alarm trim (spreaker strobe & smoke detector bas | 1 | 1 | 18-Mar-15 | 18-Mar-15 | 3 |
| LL1-Z2-8162 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 18-Mar-15 | 24-Mar-15 | 14 |
| RF-4066 | Pool Green Roof - Install decorative metal railing | 3 | 3 | 19-Mar-15 | 23-Mar-15 | 17 |
| CO-7141 | Install remaining devices & prep devices for testing - I | 7 | 7 | 19-Mar-15 | 27-Mar-15 | 10 |
| L1B-8130 | Flooring - VCT at service corridor and A/V room | 3 | 3 | 19-Mar-15 | 23-Mar-15 | 8 |
| I-1210 | Floor prep | 2 | 2 | 19-Mar-15 | 20-Mar-15 | 3 |
| L1B-8154 | Finish carpentry/millwork at corridors | 10 | 10 | 19-Mar-15 | 01-Apr-15 | 3 |
| L1L-8152 | Install ceiling (Bar) | 5 | 5 | 19-Mar-15 | 25-Mar-15 | 1 |
| CN-1000 | Install exterior canopies - steel | 5 | 5 | 19-Mar-15 | 25-Mar-15 | 13 |
| L1L-8124b | Flooring - wood - south of Grid K | 5 | 5 | 19-Mar-15 | 25-Mar-15 | 3 |
| L1BOH2-8140 | Acoustical ceiling tile | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 10 |
| L1BOH2-8201 | Paint, final coat & touch-up | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 10 |
| L1BOH2-8118 | Complete MEP trim | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 10 |
| L02-8138 | Acoustical ceiling tile at south half | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 7 |
| LL2-2088 | Lighting & electrical drops to grid at Laundry | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 3 |
| LL1-Z3-8152 | Complete MEP trim | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 10 |
| L1L-8136 | Install Peter Glassford art wall | 10 | 10 | 20-Mar-15 | 02-Apr-15 | 10 |
| LL2-2102 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 4 |
| L02-8174 | Complete MEP trim at north half | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 7 |
| L02-8176 | Paint, final coat & touch-up at north half | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 7 |
| L02-8180 | Acoustical ceiling tile at north half | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 7 |
| CO-7142 | Fire Alarm System Device Testing - Podium | 7 | 7 | 20-Mar-15 | 30-Mar-15 | 10 |
| L1K-8220 | Install countertops in restrooms | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 4 |
| L1K-8222 | Install toilet partitions | 4 | 4 | 20-Mar-15 | 25-Mar-15 | 1 |

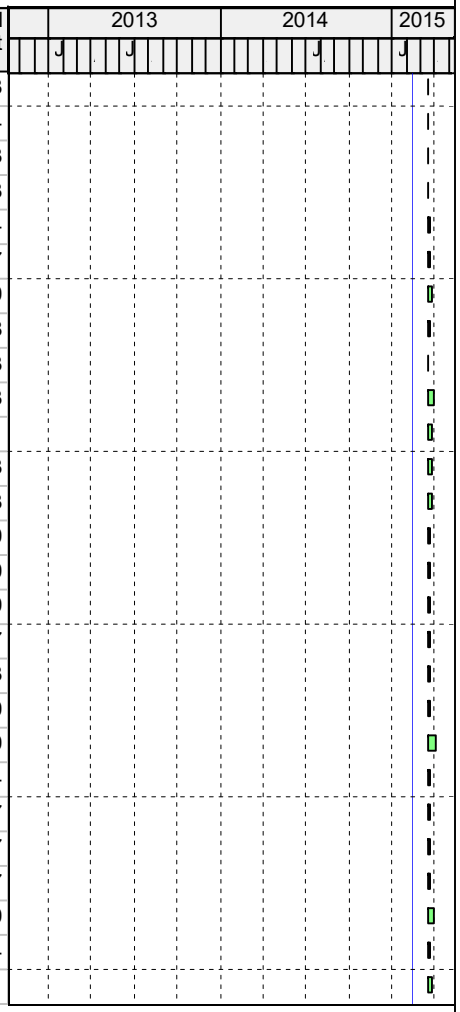



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7428 | Cx - Pressure Testing - GC Indicates Podium Comple | 0 | 0 | | 20-Mar-15 | 22 |
| I-1202 | Flooring - tile & carpet at Concierge Lounge | 6 | 6 | 23-Mar-15 | 30-Mar-15 | 3 |
| CO-7406 | Cx - FPT - MUA, RTU, VAV and Exhaust Fans | 5 | 5 | 23-Mar-15 | 27-Mar-15 | 18 |
| L03-8672 | Prep & pour pool topping slab | 2 | 2 | 23-Mar-15 | 24-Mar-15 | 2 |
| L1B-8202 | Wall coverings - vinyl at Ballrooms | 5 | 5 | 23-Mar-15 | 27-Mar-15 | 4 |
| L1K-8130 | HVAC drops/trim at celing | 2 | 2 | 23-Mar-15 | 24-Mar-15 | 5 |
| L1B-8208 | Ceiling grid at East Ballroom | 4 | 4 | 23-Mar-15 | 26-Mar-15 | 0 |
| CO-7430 | Cx - Pressure Testing - Pre-Walk with GC (Tower) | 1 | 1 | 23-Mar-15 | 23-Mar-15 | 22 |
| CM-1016a | CM - Owner FF+E "Build-Out" - Floors 3, 11-17 | 21 | 21 | 23-Mar-15 | 13-Apr-15 | 17 |
| RF-4068 | Pool Green Roof - Install American Hydrotech assemI | 3 | 3 | 24-Mar-15 | 26-Mar-15 | 17 |
| LL2-2100 | Fire sprinkler drops to grid at Laundry | 1 | 1 | 24-Mar-15 | 24-Mar-15 | 3 |
| CO-7156 | Final Inspection - Health Department (Kitchens) | 5 | 5 | 24-Mar-15 | 30-Mar-15 | 25 |
| CO-7432 | Cx - Pressure Testing - GC Makes Corrections (Tower) | 2 | 2 | 24-Mar-15 | 25-Mar-15 | 22 |
| L1BOH2-8136 | Contractor Punchlist (inspect/distribute/correct/back-pI | 5 | 5 | 24-Mar-15 | 30-Mar-15 | 10 |
| L1K-8224 | Install sinks at restrooms | 2 | 2 | 24-Mar-15 | 25-Mar-15 | 4 |
| L03-8618 | Ceramic tile at pool area | 8 | 8 | 25-Mar-15 | 03-Apr-15 | 2 |
| L03-8630 | Install doors & hardware at Pool | 2 | 2 | 25-Mar-15 | 26-Mar-15 | 14 |
| LL2-2090 | Acoustical ceiling tile at Laundry | 2 | 2 | 25-Mar-15 | 26-Mar-15 | 3 |
| LL2-2092 | Complete MEP trim at Laundry | 2 | 2 | 25-Mar-15 | 26-Mar-15 | 3 |
| L1K-8120 | Lighting & electrical trim at ceiling | 2 | 2 | 25-Mar-15 | 26-Mar-15 | 5 |
| LL2-8144 | Acoustical ceiling tile | 3 | 3 | 25-Mar-15 | 27-Mar-15 | 3 |
| L1K-8160 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 25-Mar-15 | 26-Mar-15 | 5 |
| CO-7154 | Final Inspection - Mechanical | 5 | 5 | 25-Mar-15 | 31-Mar-15 | 24 |
| LL1-Z3-8136 | Contractor Punchlist (inspect/distribute/correct/back-pI | 5 | 5 | 25-Mar-15 | 31-Mar-15 | 9 |
| L03-8640 | Prep and install pool plaster | 3 | 3 | 26-Mar-15 | 30-Mar-15 | 4 |
| MPP-1038 | Podium Signs, West | 5 | 5 | 26-Mar-15 | 01-Apr-15 | 13 |
| MPT-1074 | Tower Sign, South (El 32) | 5 | 5 | 26-Mar-15 | 01-Apr-15 | 13 |

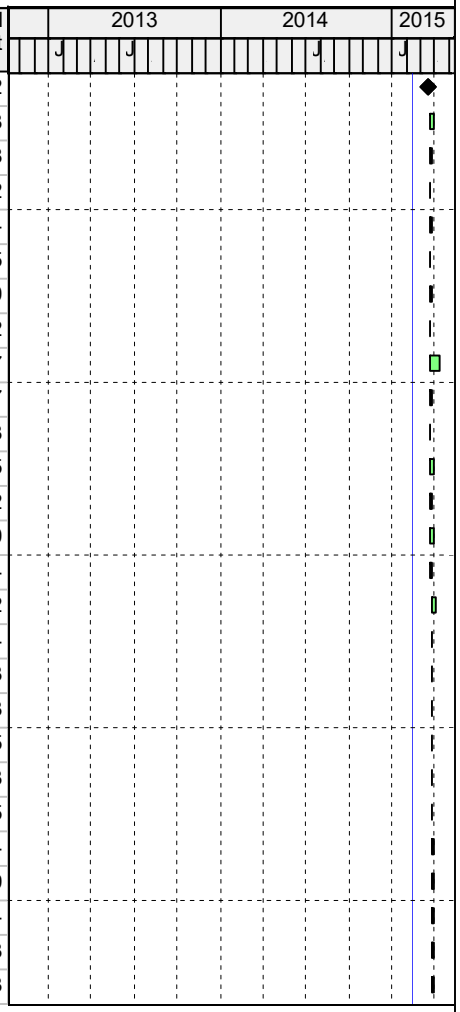



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8138 | Flooring - epoxy floor (Bar) | 5 | 5 | 26-Mar-15 | 01-Apr-15 | 1 |
| CN-1002 | Install exterior canopies - glass | 5 | 5 | 26-Mar-15 | 01-Apr-15 | 13 |
| L1L-8116a | Finish carpentry/millwork - south of Grid K | 10 | 10 | 26-Mar-15 | 08-Apr-15 | 3 |
| CO-7434 | Cx - Pressure Testing - Pressure Pre-Test (Tower) | 2 | 2 | 26-Mar-15 | 27-Mar-15 | 22 |
| CO-7112T | City of Bellevue/3rd Party Fire Sprinkler Inspection / A | 6 | 6 | 27-Mar-15 | 03-Apr-15 | 16 |
| CO-7118T | City of Bellevue/3rd Party Fire Alarm Inspection / Appl | 6 | 6 | 27-Mar-15 | 03-Apr-15 | 16 |
| CO-7106T | City of Bellevue/3rd Party Smoke Control Testing (Tow | 6 | 6 | 27-Mar-15 | 03-Apr-15 | 16 |
| L1K-8142 | Complete MEP trim | 2 | 2 | 27-Mar-15 | 30-Mar-15 | 5 |
| L1K-8122 | Fire sprinkler drops/trim at ceiling | 1 | 1 | 27-Mar-15 | 27-Mar-15 | 5 |
| L1K-8154 | Acoustical ceiling tile | 2 | 2 | 30-Mar-15 | 31-Mar-15 | 4 |
| L1K-8156 | Complete MEP trim | 2 | 2 | 30-Mar-15 | 31-Mar-15 | 4 |
| L1K-8158 | Paint, final coat & touch-up | 2 | 2 | 30-Mar-15 | 31-Mar-15 | 4 |
| LL2-8106b | Pinned insulation at ramp at Garage & dry shack area | 3 | 3 | 30-Mar-15 | 01-Apr-15 | 13 |
| CO-7436 | Cx - Pressure Testing -Corrections (Tower) | 2 | 2 | 30-Mar-15 | 31-Mar-15 | 22 |
| LL2-8154 | Contractor Punchlist (inspect/distribute/correct/back-pl | 7 | 7 | 30-Mar-15 | 07-Apr-15 | 3 |
| L02-8182 | Contractor Punchlist (inspect/distribute/correct/back-pl | 7 | 7 | 30-Mar-15 | 07-Apr-15 | 3 |
| L1BOH2-8132 | Owner Punchlist (inspect/distribute/correct/back-punch | 4 | 4 | 31-Mar-15 | 03-Apr-15 | 10 |
| I-1204 | Finish carpentry/millwork at Concierge Lounge | 10 | 10 | 31-Mar-15 | 13-Apr-15 | 3 |
| L03-8642 | Fill pool | 1 | 1 | 31-Mar-15 | 31-Mar-15 | 13 |
| L1K-8208 | Install restroom accessories | 2 | 2 | 31-Mar-15 | 01-Apr-15 | 1 |
| L1L-8282 | Finish carpentry/millwork | 5 | 5 | 31-Mar-15 | 06-Apr-15 | 8 |
| L03-8674 | Install storfront at Pool entry | 2 | 2 | 31-Mar-15 | 01-Apr-15 | 2 |
| L03-8638 | Install pool deck and ADA lift | 3 | 3 | 01-Apr-15 | 03-Apr-15 | 10 |
| L1L-8240 | Flooring - tile & base | 10 | 10 | 01-Apr-15 | 14-Apr-15 | 4 |
| L1L-8244 | Complete MEP trim | 2 | 2 | 01-Apr-15 | 02-Apr-15 | 12 |
| L1B-8129 | Floor prep | 2 | 2 | 01-Apr-15 | 02-Apr-15 | 0 |
| L1L-8288 | Paint, final coat & touch-up | 2 | 2 | 01-Apr-15 | 02-Apr-15 | 12 |

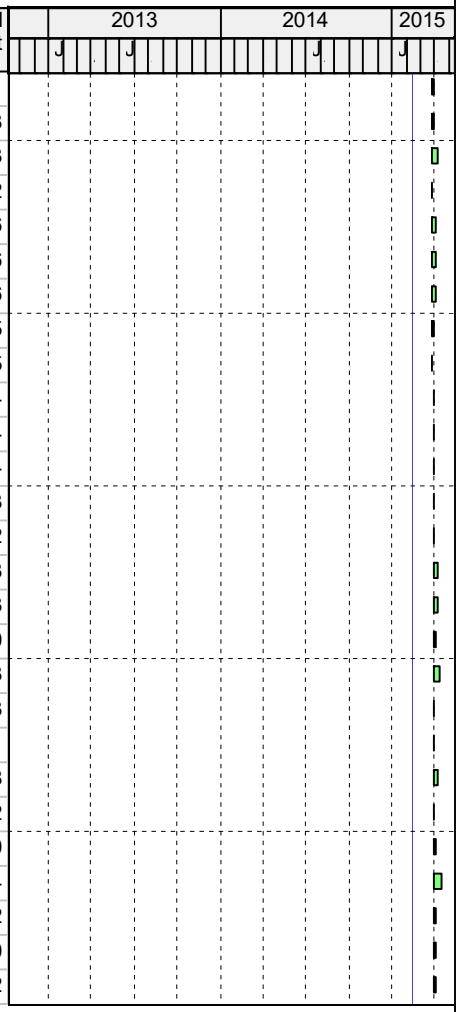



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7146 | Final Inspection - Clear & Grade | 5 | 5 | 01-Apr-15 | 07-Apr-15 | 19 |
| L1L-8130 | Install bar and back bar | 10 | 10 | 02-Apr-15 | 15-Apr-15 | 1 |
| L1K-8216 | Complete MEP trim | 2 | 2 | 02-Apr-15 | 03-Apr-15 | 1 |
| L1B-8156 | Install base at corridors | 5 | 5 | 02-Apr-15 | 08-Apr-15 | 3 |
| L1BOH2-8134 | Final Cleaning | 2 | 2 | 03-Apr-15 | 06-Apr-15 | 10 |
| L1B-8128 | Install base at Ballrooms | 5 | 5 | 03-Apr-15 | 09-Apr-15 | 0 |
| L1L-8284 | Install handrails | 2 | 2 | 03-Apr-15 | 06-Apr-15 | 8 |
| L03-8620 | Plumbing fixtures & trim at Pool | 2 | 2 | 06-Apr-15 | 07-Apr-15 | 6 |
| L03-8626 | Electrical trim & finish at Pool | 2 | 2 | 06-Apr-15 | 07-Apr-15 | 6 |
| L03-8628 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 06-Apr-15 | 07-Apr-15 | 6 |
| L03-8676 | Contractor Punchlist at Pool & Corridor (inspect/distrib | 5 | 5 | 06-Apr-15 | 10-Apr-15 | 2 |
| L1K-8166 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 06-Apr-15 | 10-Apr-15 | 1 |
| L1BOH2-81214 | L1, Zone 3 Complete | 0 | 0 | | 06-Apr-15 | 10 |
| L03-8632 | Install restroom accessories at Pool | 2 | 2 | 08-Apr-15 | 09-Apr-15 | 6 |
| L1L-8124a | Install base | 3 | 3 | 09-Apr-15 | 13-Apr-15 | 3 |
| L1B-8164 | Acoustical ceiling tile | 2 | 2 | 09-Apr-15 | 10-Apr-15 | 6 |
| L1B-8166 | Complete MEP trim | 2 | 2 | 09-Apr-15 | 10-Apr-15 | 6 |
| L1L-8203 | Complete MEP trim | 2 | 2 | 09-Apr-15 | 10-Apr-15 | 6 |
| L03-8646 | Health inspection | 1 | 1 | 10-Apr-15 | 10-Apr-15 | 6 |
| L03-8678 | Owner Punchlist at Pool & Corridor (inspect/distribute/ | 3 | 3 | 13-Apr-15 | 15-Apr-15 | 2 |
| L1L-8120 | Plumbing fixtures & trim (Bar) | 2 | 2 | 14-Apr-15 | 15-Apr-15 | 1 |
| L1L-8122 | Electrical trim & finish at bar (bar area final connectior | 2 | 2 | 14-Apr-15 | 15-Apr-15 | 1 |
| L1L-8268 | Complete MEP trim | 2 | 2 | 14-Apr-15 | 15-Apr-15 | 3 |
| L1B-8158 | Flooring - carpet at corridors | 3 | 3 | 14-Apr-15 | 16-Apr-15 | 0 |
| L1L-8300 | Paint, final coat & touch-up | 2 | 2 | 14-Apr-15 | 15-Apr-15 | 3 |
| L03-8680 | Final Cleaning at Pool & Corridor | 2 | 2 | 15-Apr-15 | 16-Apr-15 | 2 |
| LL2-8150 | LL2 Floor Complete | 0 | 0 | | 15-Apr-15 | 3 |

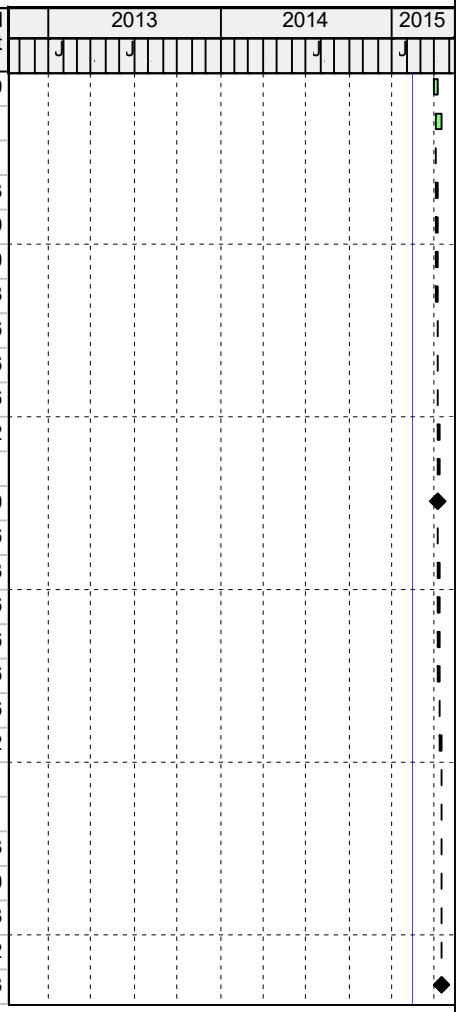



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7152 | Final Inspection - Plumbing | 5 | 5 | 16-Apr-15 | 22-Apr-15 | 8 |
| L1B-8136 | Complete MEP trim | 2 | 2 | 17-Apr-15 | 20-Apr-15 | 0 |
| L1B-8168 | Paint, final coat & touch-up | 2 | 2 | 17-Apr-15 | 20-Apr-15 | 0 |
| CO-7500 | Complete Final Walsh/WPM Inspections/Corrections | 10 | 10 | 20-Apr-15 | 01-May-15 | 1 |
| L1L-8156 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 20-Apr-15 | 24-Apr-15 | 1 |
| CO-7150 | Final Inspection - Electrical | 5 | 5 | 21-Apr-15 | 27-Apr-15 | 5 |
| L1B-8172 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 21-Apr-15 | 27-Apr-15 | 0 |
| CO-7412 | Cx - Pressure Testing - GC Indicates Podium Comple | 0 | 0 | | 21-Apr-15 | 2 |
| CO-7416 | Cx - Pressure Testing - Pre-Walk with GC (Podium) | 1 | 1 | 21-Apr-15 | 22-Apr-15 | 2 |
| CO-7418 | Cx - Pressure Testing - GC Makes Corrections (Podiu | 2 | 2 | 21-Apr-15 | 23-Apr-15 | 2 |
| CO-7420 | Cx - Pressure Testing - Pressure Pre-Test (Podium) | 2 | 2 | 23-Apr-15 | 27-Apr-15 | 2 |
| CO-7422 | Cx - Pressure Testing -Corrections (Podium) | 2 | 2 | 27-Apr-15 | 29-Apr-15 | 2 |
| CO-7424 | Cx - Pressure Testing - Pressure Final Test | 1 | 1 | 29-Apr-15 | 30-Apr-15 | 2 |
| CO-7426 | Cx - Pressure Testing - Building Final Corrections | 1 | 1 | 30-Apr-15 | 01-May-15 | 2 |
| CM-1022 | Podium - "Clean/Punch" Complete - All Floors, All Zon | 0 | 0 | | 04-May-15 | 2 |
| CO-7124 | Final Inspection - Building Department | 2 | 2 | 05-May-15 | 06-May-15 | 0 |
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13 A | | |
| CM-1002 | CM - Contract Time (578 Cal Days) | 576 | 0 | 06-Mar-13 A | 05-Oct-14 A | |
| CM-1014 | CM - Start of Construction | 0 | 0 | 05-Apr-13 A | | |
| CM-1006 | Construction Documents Issued by Client - (Due on 7 | 0 | 0 | 16-Feb-15 | | 80 |
| CM-1008 | Finalization of Allowances - (Due on 9-2-13) | 0 | 0 | 16-Feb-15 | | 80 |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 02-Mar-15* | | 13 |
| CM-1016 | CM - Owner FF+E "Build-Out" - Floors 4-10 | 21 | 21 | 02-Mar-15 | 23-Mar-15 | 17 |
| CO-7004 | CO - Prep / Submit O&M Manuals | 30 | 30 | 21-Mar-15 | 20-Apr-15 | 17 |

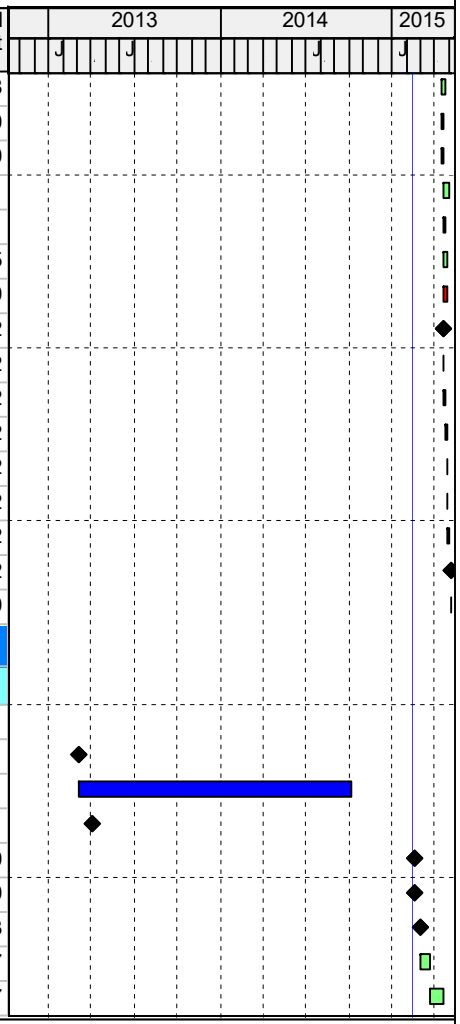


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CM-1018 | CM - Hotel Operations Training | 21 | 21 | 30-Mar-15 | 20-Apr-15 | 17 |
| CO-7006 | CO - Certificate of Occupancy/Substantial Completior | 0 | 0 | | 06-May-15 | 0 |
| CO-7122 | CO - Certificate of Occupancy | 0 | 0 | | 06-May-15 | 0 |
| **Misc Milestones** | | | | | | |
| CM-1020 | MM - Site Mobilization | 10 | 0 | 06-Mar-13 A | 04-Apr-13 A | |
| MM-1008 | MM - Top Out - Tower / Structure | 0 | 0 | | 16-Apr-14 A | |
| MM-1004 | MM - Start Drywall In Tower | 0 | 0 | 27-Jun-14 A | | |
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 06-Sep-14 A | |
| MM-1010 | Energize Permanent Power | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| Tower Crane | | | | | | |
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 0 | 04-Jun-13 A | 14-Jun-13 A | |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 0 | 20-Jun-13 A | 24-Jun-13 A | |
| TC-5902 | Tower Crane - Erectiion | 2 | 0 | 21-Jun-13 A | 24-Jun-13 A | |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 24-Jun-13 A | | |
| TC-5906 | Tower Crane - Operatational Period | 391 | 0 | 24-Jun-13 A | 16-Jun-14 A | |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 0 | 16-Jun-14 A | 17-Jun-14 A | |
| Man & Material Lifts | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 0 | 14-Jan-14 A | 20-Jan-14 A | |
| ML-5952 | Man/Material Lifts - Erect/Build Loading Dock | 5 | 0 | 21-Jan-14 A | 27-Jan-14 A | |
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 10-Feb-14 A | | |
| ML-5954 | Man/Material Lifts - Load Test / Certify | 1 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| ML-5958 | Man/Material Lifts - Operatational Period | 196 | 0 | 10-Feb-14 A | 15-Nov-14 A | |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 2 | 0 | 15-Nov-14 A | 16-Nov-14 A | |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |

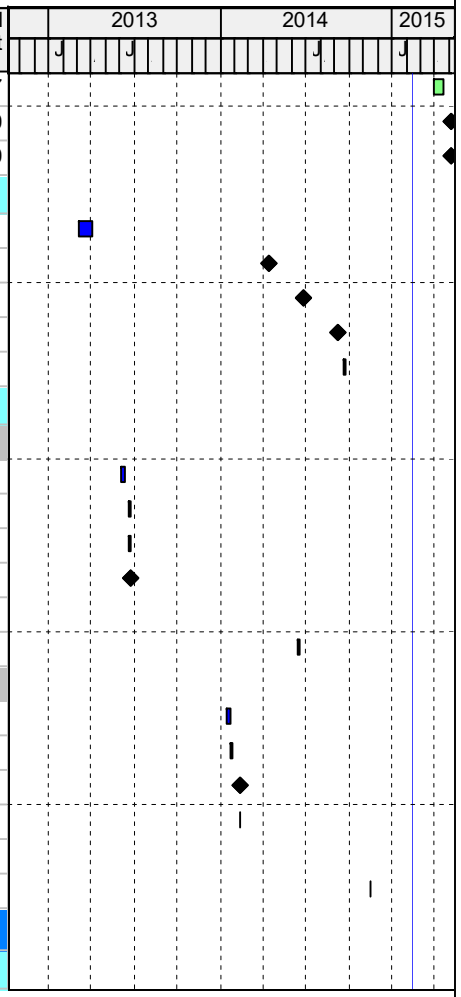



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Mass Excavation / Shoring** | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 0 | 05-Apr-13 A | 12-Apr-13 A | |
| SW-2002 | Demolition And Utility Relocation | 8 | 0 | 15-Apr-13 A | 19-Apr-13 A | |
| SW-2010 | Grade Subgrade for Elect/Plumbing | 3 | 0 | 07-Jan-14 A | 09-Jan-14 A | |
| **Site Finishes** | | | | | | |
| SW-2006 | Install Perm Power Electrical Service / Dry Utilities (Ofl | 15 | 0 | 20-May-14 A | 05-Jun-14 A | |
| SW-2004 | Offsite Water & Water Connection | 9 | 0 | 22-Sep-14 A | 01-Oct-14 A | |
| SW-2008 | Zone 4 - Landscaping & irrigation | 7 | 7 | 23-Mar-15 | 31-Mar-15 | 19 |
| **Structure** | | | | | | |
| **Foundation / Substructure - (Levels LL4 / LL3)** | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 0 | 12-Jun-13 A | 27-Jun-13 A | |
| LL4-1601 | LL4 - Excavate Footings | 14 | 0 | 17-Jun-13 A | 30-Jul-13 A | |
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 0 | 18-Jun-13 A | 24-Jun-13 A | |
| LL4-1606 | LL4 - Undrgmd Plumbing | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-1608 | LL4 - Undrgmd Elec | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 0 | 19-Jun-13 A | 25-Jun-13 A | |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 0 | 26-Jun-13 A | 02-Aug-13 A | |
| LL4-2033 | LL4 - Shotcrete Walls | 27 | 0 | 26-Jun-13 A | 05-Aug-13 A | |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 0 | 03-Jul-13 A | 21-Aug-13 A | |
| LL4-1614 | LL4 - FRP SOG | 5 | 0 | 10-Jul-13 A | 07-Aug-13 A | |
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 0 | 12-Jul-13 A | 26-Jul-13 A | |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 0 | 13-Jul-13 A | 06-Aug-13 A | |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 0 | 22-Jul-13 A | 24-Jul-13 A | |
| LL4-1618 | LL4 - FRP Ramp SOG | 5 | 0 | 01-Aug-13 A | 07-Aug-13 A | |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2004 | LL2 - Shore / Form Deck | 8 | 0 | 05-Aug-13 A | 09-Aug-13 A | |

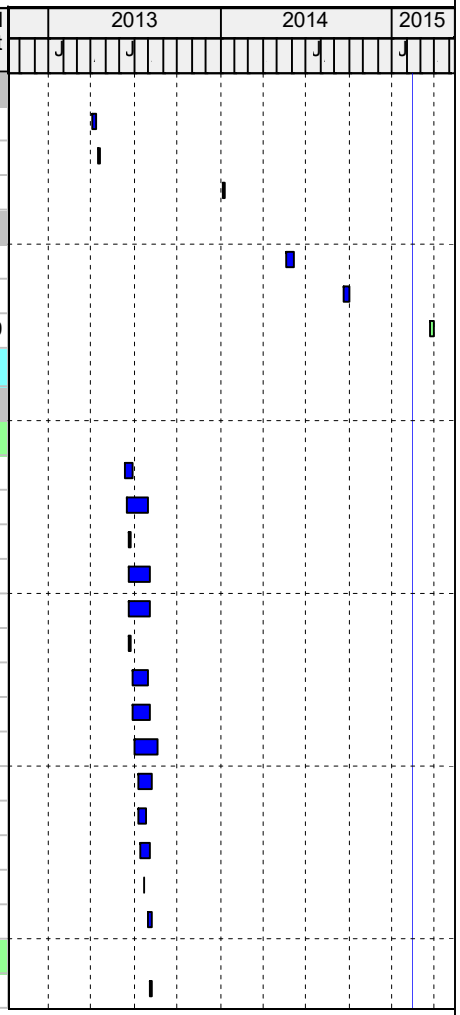


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-2006 | LL3 - M & E Inserts | 4 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2008 | LL3 - ReSteel / PT Cables | 6 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2010 | LL3 - Install Embeds | 2 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2001 | LL3 - Waterproof Walls | 3 | 0 | 05-Aug-13 A | 05-Aug-13 A | |
| LL3-2012 | LL3 - Pour / Finish Deck | 2 | 0 | 16-Aug-13 A | 16-Aug-13 A | |
| LL3-2014 | LL3 - Stress Tendons | 1 | 0 | 19-Aug-13 A | 19-Aug-13 A | |
| LL3-2000 | LL3 - FRP Core Walls | 8 | 0 | 19-Aug-13 A | 28-Aug-13 A | |
| LL3-2033 | LL3 - Shotcrete Walls | 5 | 0 | 23-Aug-13 A | 26-Aug-13 A | |
| LL3-2016 | LL3 - Strip / ReShore Deck | 3 | 0 | 01-Sep-13 A | 13-Sep-13 A | |
| LL3-2018 | LL3 - Remove ReShores | 4 | 0 | 04-Nov-13 A | 07-Nov-13 A | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Grids 1 to 4 - (SOG @ Loading Dock)** | | | | | | |
| LL2-2056 | LL2 - Grease Intercepter | 5 | 0 | 15-Aug-13 A | 21-Aug-13 A | |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 0 | 27-Aug-13 A | 04-Sep-13 A | |
| LL2-2027 | LL2 - Waterproof Walls | 2 | 0 | 27-Aug-13 A | 28-Aug-13 A | |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 0 | 30-Aug-13 A | 05-Sep-13 A | |
| LL2-2021 | LL2 - FRP Elec Vault | 14 | 0 | 30-Aug-13 A | 04-Sep-13 A | |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 0 | 04-Sep-13 A | 11-Sep-13 A | |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 0 | 11-Sep-13 A | 13-Sep-13 A | |
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls/Roof | 11 | 0 | 19-Sep-13 A | 03-Oct-13 A | |
| LL2-2020 | LL2 - Undrgmd Plumbing | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2022 | LL2 - Undrgmd Elec | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2031 | LL2 - FRP Generator SOG | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2015 | LL2 to LL1 FRP Columns / Misc Walls | 6 | 0 | 01-Oct-13 A | 01-Oct-13 A | |
| LL2-2029 | LL2 - F/R/P Pour #2 | 8 | 0 | 15-Jan-14 A | 24-Jan-14 A | |

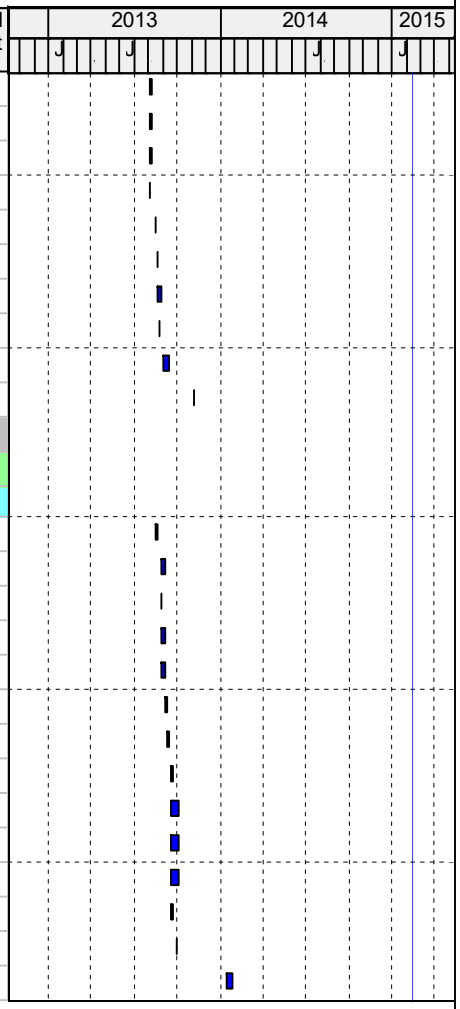



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2011 | LL2 - F/R/P Pour #3 | 16 | 0 | 24-Jan-14 A | 18-Feb-14 A | |
| LL2-2019 | LL2 - F/R/P Pour #6 | 4 | 0 | 19-Feb-14 A | 17-Mar-14 A | |
| LL2-2044 | LL2 - Set Generator | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |
| LL2-2004 | LL2 - Shore / Form Deck | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2035 | LL2 to LL1 - Shotcrete Walls | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2006 | LL2 - M & E Inserts | 4 | 0 | 14-Aug-13 A | 19-Aug-13 A | |
| LL2-2008 | LL2 - ReSteel / PT Cables | 6 | 0 | 14-Aug-13 A | 21-Aug-13 A | |
| LL2-2010 | LL2 - Install Embeds | 3 | 0 | 14-Aug-13 A | 16-Aug-13 A | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 0 | 27-Aug-13 A | 06-Sep-13 A | |
| LL2-2012 | LL2 - Place / Finish Deck | 3 | 0 | 29-Aug-13 A | 29-Aug-13 A | |
| LL2-2023 | LL2 - Waterproof Walls | 3 | 0 | 29-Aug-13 A | 03-Sep-13 A | |
| LL2-2014 | LL2 - Stress Tendons | 1 | 0 | 30-Aug-13 A | 30-Aug-13 A | |
| LL2-2016 | LL2 - Strip / ReShore | 3 | 0 | 03-Sep-13 A | 05-Sep-13 A | |
| LL2-8234 | LL2 - Place / Finish Deck | 3 | 0 | 12-Sep-13 A | 12-Sep-13 A | |
| LL2-2000 | LL2 - FRP Core Walls | 8 | 0 | 12-Sep-13 A | 23-Sep-13 A | |
| LL2-2018 | LL2 - Remove ReShores | 4 | 0 | 13-Nov-13 A | 18-Nov-13 A | |
| LL2-2013 | LL2 - F/R/P Pour #1 | 4 | 0 | 13-Jan-14 A | 16-Jan-14 A | |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| P5A-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2000 | LL1 - FRP Core Walls | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2004 | LL1 - Shore / Form Deck | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| P6-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P6-2004 | LL1 - Shore / Form Deck | 7 | 0 | 16-Sep-13 A | 24-Sep-13 A | |
| P5A-2006 | LL1 - MEP Rough In | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2008 | LL1 - ReSteel / PT Cables | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |

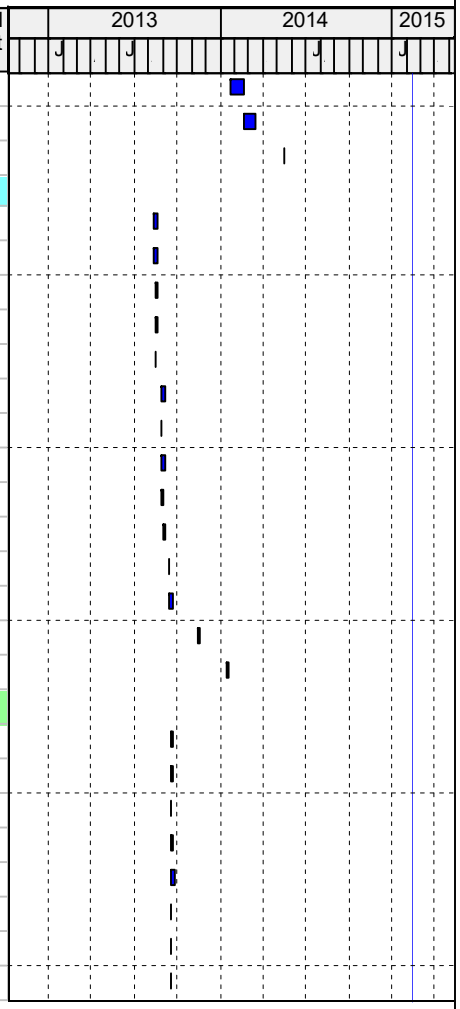



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P5A-2012 | LL1 - Place / Finish Deck | 0 | 0 | 20-Sep-13 A | | |
| P5A-2020 | LL1 - Waterproof Walls | 3 | 0 | 20-Sep-13 A | 24-Sep-13 A | |
| P5A-2014 | LL1 - Stress Tendons | 1 | 0 | 23-Sep-13 A | 23-Sep-13 A | |
| P5A-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2006 | LL1 - MEP Rough In | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2008 | LL1 - ReSteel / PT Cables | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 24-Sep-13 A | 25-Sep-13 A | |
| P6-2020 | LL1 - Waterproof Walls | 4 | 0 | 24-Sep-13 A | 27-Sep-13 A | |
| P5A-2033 | LL1 - Resteel/Shotcrete Walls | 3 | 0 | 25-Sep-13 A | 27-Sep-13 A | |
| P5B-2002 | LL1 - FRP Columns Below | 5 | 0 | 26-Sep-13 A | 02-Oct-13 A | |
| P5B-2004 | LL1 - Shore / Form Deck | 7 | 0 | 26-Sep-13 A | 04-Oct-13 A | |
| P6-2012 | LL1 - Place / Finish Deck | 0 | 0 | 27-Sep-13 A | | |
| P6-2014 | LL1 - Stress Tendons | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2033 | LL1 - Resteel/Shotcrete Walls | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 01-Oct-13 A | 03-Oct-13 A | |
| P5B-2006 | LL1 - MEP Rough In | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2002 | FRP Columns Below | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2004 | Shore / Form Deck | 4 | 0 | 03-Oct-13 A | 08-Oct-13 A | |
| P5B-2008 | LL1 - ReSteel / PT Cables | 5 | 0 | 04-Oct-13 A | 10-Oct-13 A | |
| P5B-2010 | LL1 - Install Edgeform/Embeds | 4 | 0 | 04-Oct-13 A | 09-Oct-13 A | |
| P8-2002 | FRP Columns Below | 5 | 0 | 07-Oct-13 A | 11-Oct-13 A | |
| P8-2000 | Form/Resteel/Close Core Walls | 14 | 0 | 07-Oct-13 A | 24-Oct-13 A | |
| P8-2004 | Shore / Form Deck P8 | 8 | 0 | 07-Oct-13 A | 16-Oct-13 A | |
| P7-2002 | FRP Columns Below | 5 | 0 | 08-Oct-13 A | 14-Oct-13 A | |
| P7-2004 | Shore / Form Deck | 6 | 0 | 08-Oct-13 A | 15-Oct-13 A | |
| P10A--2006 | MEP Rough In | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2008 | ReSteel / PT Cables | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |

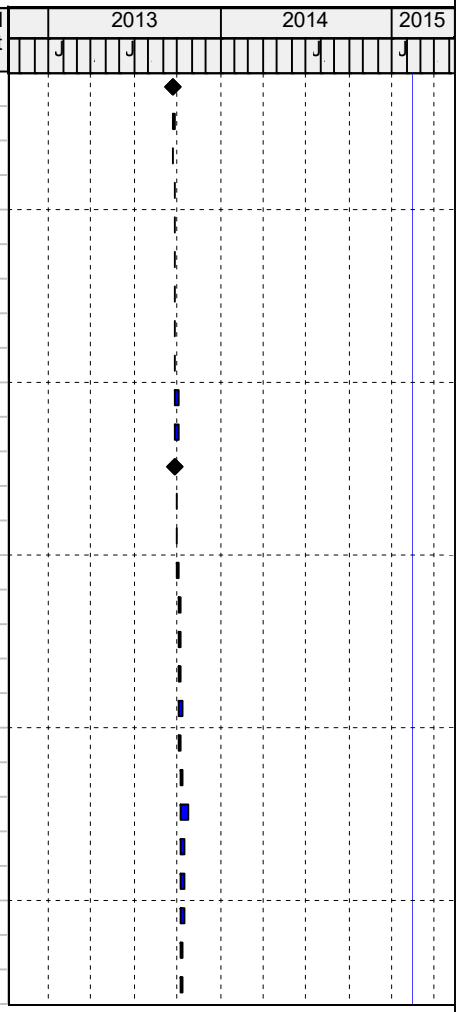


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P10A--2010 | Install Edgeform/Embeds | 2 | 0 | 08-Oct-13 A | 09-Oct-13 A | |
| P5B-2012 | LL1 - Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P10A--2012 | Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P5B-2014 | LL1 - Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P7-2006 | MEP Rough In | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P7-2008 | ReSteel / PT Cables | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P10A--2014 | Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P8-2020 | Shore / Form Deck P9 | 6 | 0 | 14-Oct-13 A | 21-Oct-13 A | |
| P5B-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2010 | Install Edgeform/Embeds | 2 | 0 | 15-Oct-13 A | 16-Oct-13 A | |
| P8-2006 | MEP Rough In | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2008 | ReSteel / PT Cables | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2010 | Install Edgeform/Embeds | 4 | 0 | 15-Oct-13 A | 18-Oct-13 A | |
| P10A--2016 | Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2012 | Place / Finish Deck | 0 | 0 | 18-Oct-13 A | | |
| P7-2033 | Resteel/Shotcrete Walls | 3 | 0 | 18-Oct-13 A | 22-Oct-13 A | |
| P7-2014 | Stress Tendons | 1 | 0 | 21-Oct-13 A | 21-Oct-13 A | |
| P7-2016 | Strip / ReShore Deck | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2002 | FRP Columns Below | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P10B--2000 | FRP Shear Walls Below | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2004 | Shore / Form Deck | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P8-2012 | Place / Finish Deck P 8 & 9 and Core Walls | 0 | 0 | 25-Oct-13 A | | |
| P8-2014 | Stress Tendons | 1 | 0 | 28-Oct-13 A | 28-Oct-13 A | |
| P10B--2006 | MEP Rough In | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2008 | ReSteel / PT Cables | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2010 | Install Edgeform/Embeds | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P12--2002 | FRP Columns Below | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |

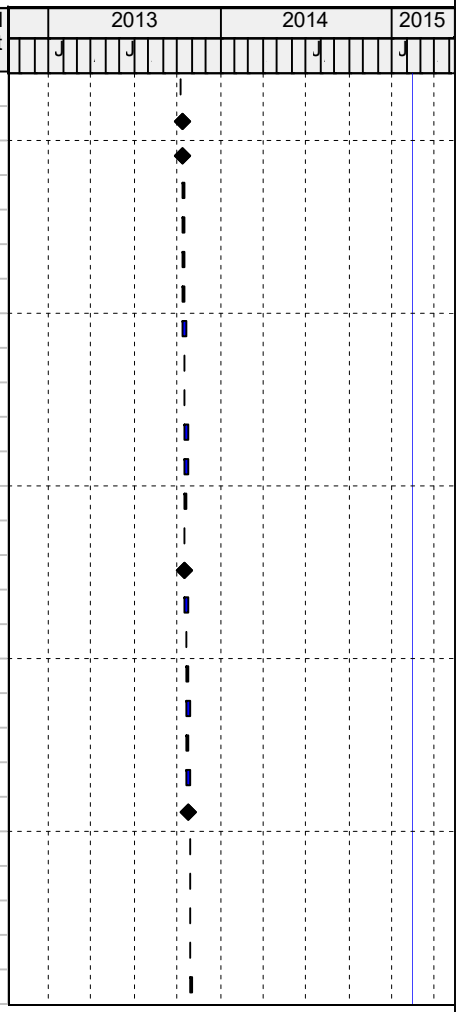



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P12–2000 | Form/Resteel/Close Core Walls | 9 | 0 | 28-Oct-13 A | 07-Nov-13 A | |
| P12–2004 | Shore / Form Deck | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P8-2016 | Strip / ReShore Deck | 3 | 0 | 29-Oct-13 A | 31-Oct-13 A | |
| P11–2002 | FRP Columns Below | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P11–2004 | Shore / Form Deck | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P10B–2012 | Place / Finish Deck | 0 | 0 | 31-Oct-13 A | | |
| P10B–2014 | Stress Tendons | 1 | 0 | 01-Nov-13 A | 01-Nov-13 A | |
| P12–2006 | MEP Rough In | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12–2008 | ReSteel / PT Cables | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12–2010 | Install Edgeform/Embeds | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P10B–2016 | Strip / ReShore Deck | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2006 | MEP Rough In | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2008 | ReSteel / PT Cables | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2010 | Install Edgeform/Embeds | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2012 | Place / Finish Deck | 0 | 0 | 07-Nov-13 A | | |
| P13–2002 | FRP Columns Below | 5 | 0 | 07-Nov-13 A | 14-Nov-13 A | |
| P13–2004 | Shore / Form Deck | 9 | 0 | 07-Nov-13 A | 28-Nov-13 A | |
| P11–2014 | Stress Tendons | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| P12–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 08-Nov-13 A | | |
| P11–2016 | Strip / ReShore Deck | 3 | 0 | 12-Nov-13 A | 14-Nov-13 A | |
| P12–2014 | Stress Tendons | 1 | 0 | 12-Nov-13 A | 12-Nov-13 A | |
| P14–2002 | FRP Columns Below | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P14–2000 | Form/Resteel/Close Core Walls | 8 | 0 | 19-Nov-13 A | 03-Dec-13 A | |
| P14–2004 | Shore / Form Deck | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P13A–2002 | FRP Columns Below | 5 | 0 | 21-Nov-13 A | 27-Nov-13 A | |
| P13A–2004 | Shore / Form Deck | 4 | 0 | 21-Nov-13 A | 26-Nov-13 A | |
| P13–2010 | Install Edgeform/Embeds | 5 | 0 | 22-Nov-13 A | 04-Dec-13 A | |

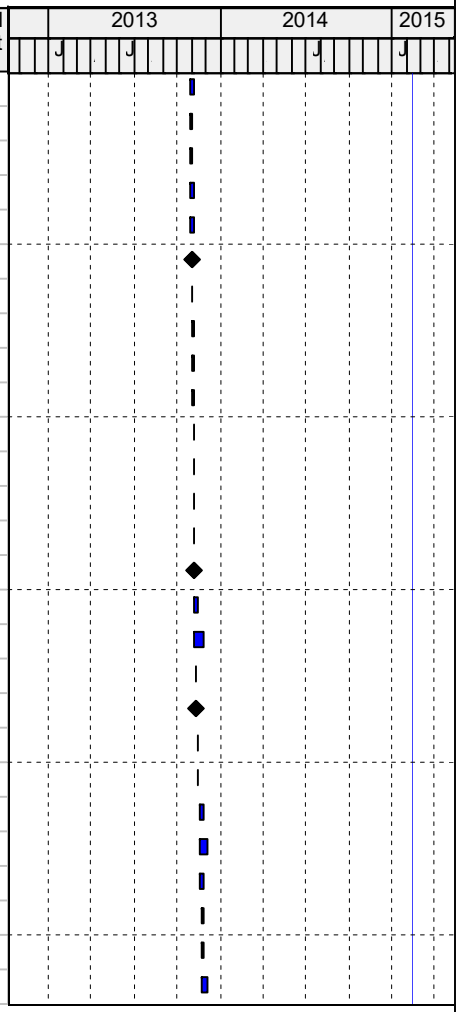



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P13–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2006 | MEP Rough In | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2010 | Install Edgeform/Embeds | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P13–2006 | MEP Rough In | 5 | 0 | 26-Nov-13 A | 03-Dec-13 A | |
| P13A–2006 | MEP Rough In | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2008 | ReSteel / PT Cables | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2010 | Install Edgeform/Embeds | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13–2012 | Place / Finish Deck | 0 | 0 | 02-Dec-13 A | | |
| P13A–2012 | Place / Finish Deck | 0 | 0 | 03-Dec-13 A | | |
| P14–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 04-Dec-13 A | | |
| P13–2014 | Stress Tendons | 1 | 0 | 05-Dec-13 A | 05-Dec-13 A | |
| P15–2002 | FRP Columns Below | 3 | 0 | 05-Dec-13 A | 09-Dec-13 A | |
| P15–2000 | Jump/Resteel/Close Core | 9 | 0 | 05-Dec-13 A | 17-Dec-13 A | |
| P15–2004 | Shore / Form Deck | 5 | 0 | 05-Dec-13 A | 11-Dec-13 A | |
| P13–2016 | Strip / ReShore Deck | 3 | 0 | 06-Dec-13 A | 10-Dec-13 A | |
| P13A–2014 | Stress Tendons | 1 | 0 | 06-Dec-13 A | 06-Dec-13 A | |
| P14–2014 | Stress Tendons | 1 | 0 | 07-Dec-13 A | 07-Dec-13 A | |
| P15–2006 | MEP Rough In | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2008 | ReSteel / PT Cables | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2010 | Install Edgeform/Embeds | 3 | 0 | 11-Dec-13 A | 13-Dec-13 A | |
| P16-2002 | FRP Columns Below | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P16-2004 | Shore / Form Deck | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P15–2012 | Place / Finish Deck | 0 | 0 | 18-Dec-13 A | | |
| P15–2020 | Place Conc @ Core | 0 | 0 | 18-Dec-13 A | | |
| P16-2000 | Jump/Resteel/Close Core | 5 | 0 | 18-Dec-13 A | 24-Dec-13 A | |
| P16-2006 | MEP Rough In | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |

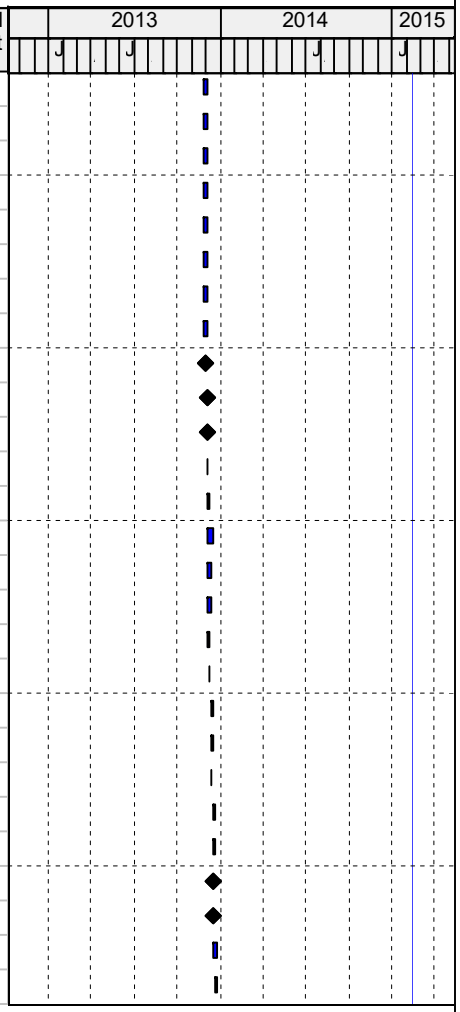



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P16-2008 | ReSteel / PT Cables | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2010 | Install Edgeform/Embeds | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P15--2014 | Stress Tendons | 1 | 0 | 21-Dec-13 A | 21-Dec-13 A | |
| P8-2018 | Remove Reshores | 2 | 0 | 23-Dec-13 A | 24-Dec-13 A | |
| P10A--2018 | Remove Reshores | 2 | 0 | 26-Dec-13 A | 27-Dec-13 A | |
| P16-2012 | Place / Finish Deck | 0 | 0 | 26-Dec-13 A | | |
| P16-2020 | Place Conc @ Core | 0 | 0 | 26-Dec-13 A | | |
| P17-2002 | FRP Columns Below | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P17-2000 | Jump/Resteel/Close Core | 7 | 0 | 27-Dec-13 A | 07-Jan-14 A | |
| P17-2004 | Shore / Form Deck | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P10B--2018 | Remove Reshores | 2 | 0 | 30-Dec-13 A | 31-Dec-13 A | |
| P16-2014 | Stress Tendons | 1 | 0 | 31-Dec-13 A | 31-Dec-13 A | |
| P5A-2018 | LL1 - Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P11--2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P12--2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P17-2006 | MEP Rough In | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2008 | ReSteel / PT Cables | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2010 | Install Edgeform/Embeds | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P6-2018 | LL1 - Remove Reshores | 2 | 0 | 06-Jan-14 A | 07-Jan-14 A | |
| P5B-2018 | LL1 - Remove Reshores | 2 | 0 | 08-Jan-14 A | 09-Jan-14 A | |
| P17-2012 | Place / Finish Deck | 0 | 0 | 08-Jan-14 A | | |
| P17-2020 | Place Conc @ Core | 0 | 0 | 08-Jan-14 A | | |
| P18-2002 | FRP Columns Below | 5 | 0 | 09-Jan-14 A | 15-Jan-14 A | |
| P18-2000 | Jump/Resteel/Close Core | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P18-2004 | Shore / Form Deck | 3 | 0 | 09-Jan-14 A | 13-Jan-14 A | |
| LL2-2022R | MEP Rough In | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P7-2018 | Remove Reshores | 2 | 0 | 10-Jan-14 A | 13-Jan-14 A | |

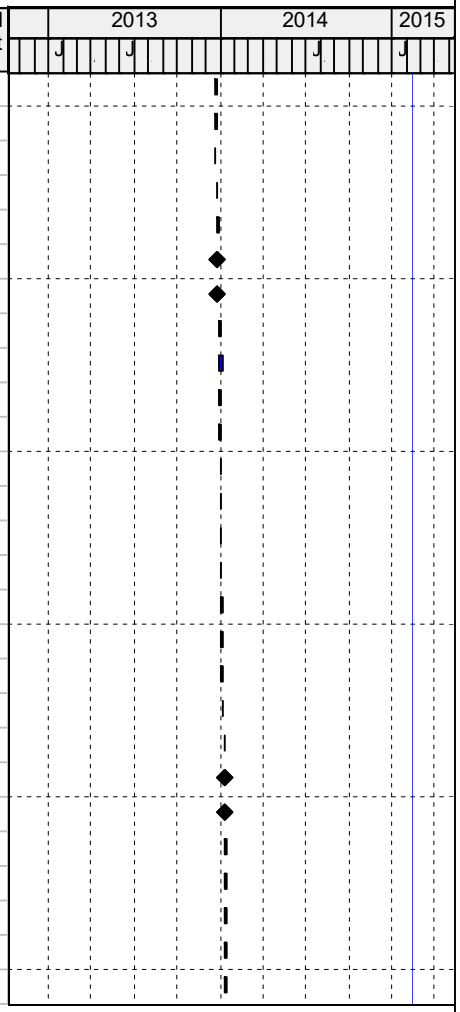



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P17-2014 | Stress Tendons | 1 | 0 | 11-Jan-14 A | 11-Jan-14 A | |
| P13–2018 | Remove Reshores | 2 | 0 | 13-Jan-14 A | 14-Jan-14 A | |
| P13A–2018 | Remove Reshores | 2 | 0 | 15-Jan-14 A | 16-Jan-14 A | |
| WEA-2012 | WIND IMPACT | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| P18-2006 | MEP Rough In | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2008 | ReSteel / PT Cables | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2010 | Install Edgeform/Embeds | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2012 | Place / Finish Deck | 0 | 0 | 22-Jan-14 A | | |
| P18-2020 | Place Conc @ Core | 0 | 0 | 22-Jan-14 A | | |
| P19-2002 | FRP Columns Below | 5 | 0 | 23-Jan-14 A | 29-Jan-14 A | |
| P19-2000 | Jump/Resteel/Close Core | 4 | 0 | 23-Jan-14 A | 28-Jan-14 A | |
| P19-2004 | Shore / Form Deck | 3 | 0 | 23-Jan-14 A | 27-Jan-14 A | |
| P18-2014 | Stress Tendons | 1 | 0 | 25-Jan-14 A | 25-Jan-14 A | |
| P14–2018 | Remove Reshores | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2006 | MEP Rough In | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2008 | ReSteel / PT Cables | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2010 | Install Edgeform/Embeds | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2012 | Place / Finish Deck | 0 | 0 | 29-Jan-14 A | | |
| P19-2020 | Place Conc @ Core | 0 | 0 | 29-Jan-14 A | | |
| P20-2002 | FRP Columns Below | 5 | 0 | 30-Jan-14 A | 05-Feb-14 A | |
| P20-2000 | Jump/Resteel/Close Core | 9 | 0 | 30-Jan-14 A | 11-Feb-14 A | |
| P20-2004 | Shore / Form Deck | 6 | 0 | 30-Jan-14 A | 10-Feb-14 A | |
| P19-2014 | Stress Tendons | 1 | 0 | 01-Feb-14 A | 01-Feb-14 A | |
| P13A–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P14–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P15–2016 | Strip / ReShore Deck | 3 | 0 | 06-Feb-14 A | 10-Feb-14 A | |
| P20-2006 | MEP Rough In | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |

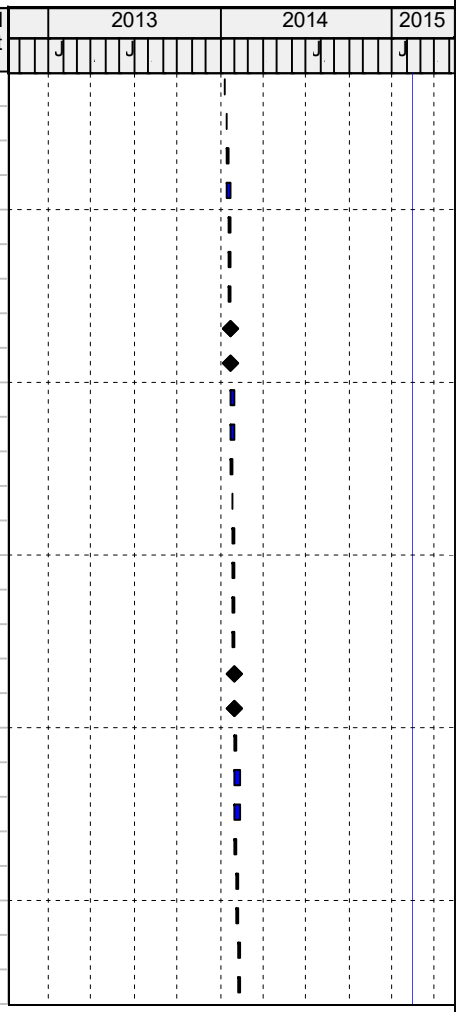



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P20-2008 | ReSteel / PT Cables | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2010 | Install Edgeform/Embeds | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| L03-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 06-Feb-14 A | 12-Feb-14 A | |
| P16-2016 | Strip / ReShore Deck | 3 | 0 | 10-Feb-14 A | 12-Feb-14 A | |
| L04-2018 | Remove Reshores | 2 | 0 | 10-Feb-14 A | 11-Feb-14 A | |
| L03-2018 | Remove Reshores | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| P17-2016 | Strip / ReShore Deck | 3 | 0 | 12-Feb-14 A | 14-Feb-14 A | |
| P20-2012 | Place / Finish Deck | 0 | 0 | 12-Feb-14 A | | |
| P20-2020 | Place Conc @ Core | 0 | 0 | 12-Feb-14 A | | |
| L04-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-Feb-14 A | 18-Feb-14 A | |
| P12–2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P18-2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P21-2002 | FRP Columns Below | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| P21-2000 | Jump/Resteel/Close Core | 4 | 0 | 13-Feb-14 A | 18-Feb-14 A | |
| P21-2004 | Shore / Form Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P19-2016 | Strip / ReShore Deck | 3 | 0 | 14-Feb-14 A | 18-Feb-14 A | |
| P20-2014 | Stress Tendons | 1 | 0 | 15-Feb-14 A | 15-Feb-14 A | |
| P21-2006 | MEP Rough In | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2008 | ReSteel / PT Cables | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P20-2016 | Strip / ReShore Deck | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| L05-2018 | Remove Reshores | 2 | 0 | 18-Feb-14 A | 19-Feb-14 A | |
| P21-2012 | Place / Finish Deck | 0 | 0 | 19-Feb-14 A | | |
| P21-2020 | Place Conc @ Core | 0 | 0 | 19-Feb-14 A | | |
| P22-2002 | FRP Columns Below | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P22-2000 | Jump/Resteel/Close Core | 4 | 0 | 20-Feb-14 A | 25-Feb-14 A | |
| P22-2004 | Shore / Form Deck | 3 | 0 | 20-Feb-14 A | 24-Feb-14 A | |

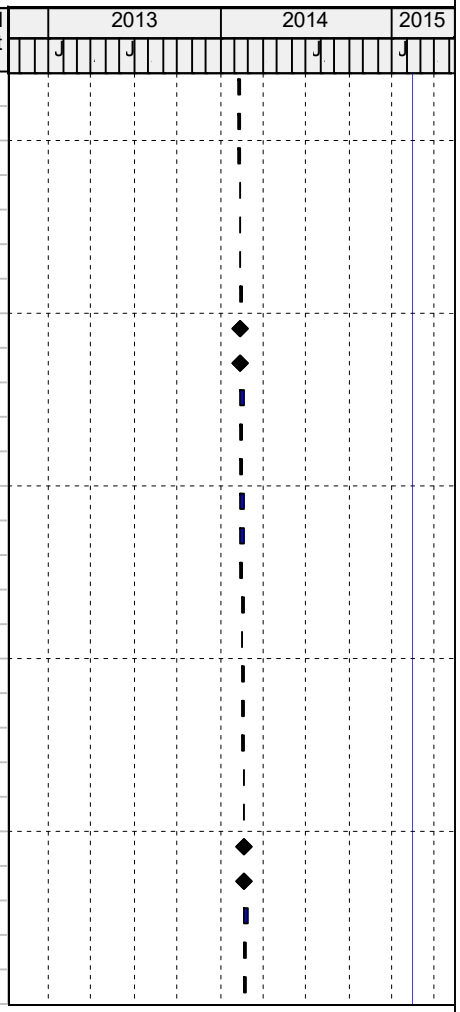


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P21-2014 | Stress Tendons | 1 | 0 | 22-Feb-14 A | 22-Feb-14 A | |
| P21-2016 | Strip / ReShore Deck | 3 | 0 | 24-Feb-14 A | 26-Feb-14 A | |
| P22-2006 | MEP Rough In | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2008 | ReSteel / PT Cables | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| L06-2018 | Remove Reshores | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| P22-2012 | Place / Finish Deck | 0 | 0 | 26-Feb-14 A | | |
| P22-2020 | Place Conc @ Core | 0 | 0 | 26-Feb-14 A | | |
| P23-2002 | FRP Columns Below | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2000 | Jump/Resteel/Close Core | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2004 | Shore / Form Deck | 3 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2006 | MEP Rough In | 2 | 0 | 01-Mar-14 A | 03-Mar-14 A | |
| P22-2014 | Stress Tendons | 1 | 0 | 01-Mar-14 A | 01-Mar-14 A | |
| P23-2008 | ReSteel / PT Cables | 2 | 0 | 03-Mar-14 A | 04-Mar-14 A | |
| P22-2016 | Strip / ReShore Deck | 3 | 0 | 04-Mar-14 A | 10-Mar-14 A | |
| P23-2010 | Install Edgeform/Embeds | 2 | 0 | 04-Mar-14 A | 04-Mar-14 A | |
| L07-2018 | Remove Reshores | 2 | 0 | 04-Mar-14 A | 05-Mar-14 A | |
| P23-2012 | Place / Finish Deck | 0 | 0 | 05-Mar-14 A | | |
| P23-2020 | Place Conc @ Core | 0 | 0 | 05-Mar-14 A | | |
| P24-2002 | FRP Columns Below | 5 | 0 | 05-Mar-14 A | 07-Mar-14 A | |
| P24-2004 | Shore / Form Deck | 3 | 0 | 06-Mar-14 A | 10-Mar-14 A | |
| P24-2000 | Jump/Resteel/Close Core | 4 | 0 | 08-Mar-14 A | 10-Mar-14 A | |
| P23-2014 | Stress Tendons | 1 | 0 | 10-Mar-14 A | 10-Mar-14 A | |
| P24-2008 | ReSteel / PT Cables | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P24-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P23-2016 | Strip / ReShore Deck | 3 | 0 | 11-Mar-14 A | 17-Mar-14 A | |

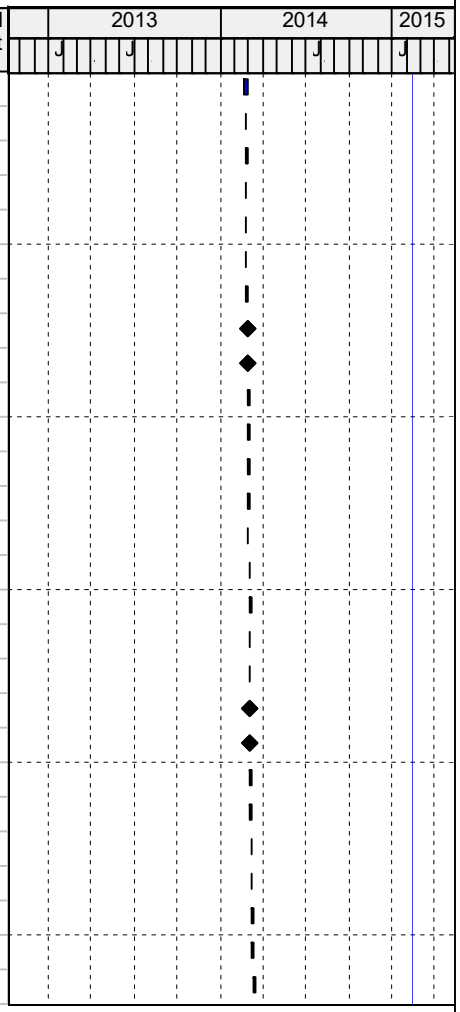



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P24-2006 | MEP Rough In | 2 | 0 | 11-Mar-14 A | 11-Mar-14 A | |
| P25-2002 | FRP Columns Below | 5 | 0 | 11-Mar-14 A | 13-Mar-14 A | |
| L08-2018 | Remove Reshores | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| P24-2012 | Place / Finish Deck | 0 | 0 | 12-Mar-14 A | | |
| P24-2020 | Place Conc @ Core | 0 | 0 | 12-Mar-14 A | | |
| P25-2004 | Shore / Form Deck | 3 | 0 | 13-Mar-14 A | 17-Mar-14 A | |
| P25-2000 | Jump/Resteel/Close Core | 4 | 0 | 15-Mar-14 A | 17-Mar-14 A | |
| P24-2014 | Stress Tendons | 1 | 0 | 17-Mar-14 A | 17-Mar-14 A | |
| P25-2006 | MEP Rough In | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2008 | ReSteel / PT Cables | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| L06-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 18-Mar-14 A | 20-Mar-14 A | |
| L09-2018 | Remove Reshores | 2 | 0 | 18-Mar-14 A | 19-Mar-14 A | |
| P26-2002 | FRP Columns Below | 5 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| P25-2012 | Place / Finish Deck | 0 | 0 | 19-Mar-14 A | | |
| P25-2020 | Place Conc @ Core | 0 | 0 | 19-Mar-14 A | | |
| P26-2004 | Shore / Form Deck | 3 | 0 | 20-Mar-14 A | 24-Mar-14 A | |
| L07-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 21-Mar-14 A | 25-Mar-14 A | |
| P26-2000 | Jump/Resteel/Close Core | 4 | 0 | 22-Mar-14 A | 24-Mar-14 A | |
| P26-2006 | MEP Rough In | 2 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P26-2008 | ReSteel / PT Cables | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P26-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P25-2014 | Stress Tendons | 1 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P27-2002 | FRP Columns Below | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| P26-2012 | Place / Finish Deck | 0 | 0 | 26-Mar-14 A | | |
| P26-2020 | Place Conc @ Core | 0 | 0 | 26-Mar-14 A | | |
| L08-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 26-Mar-14 A | 28-Mar-14 A | |

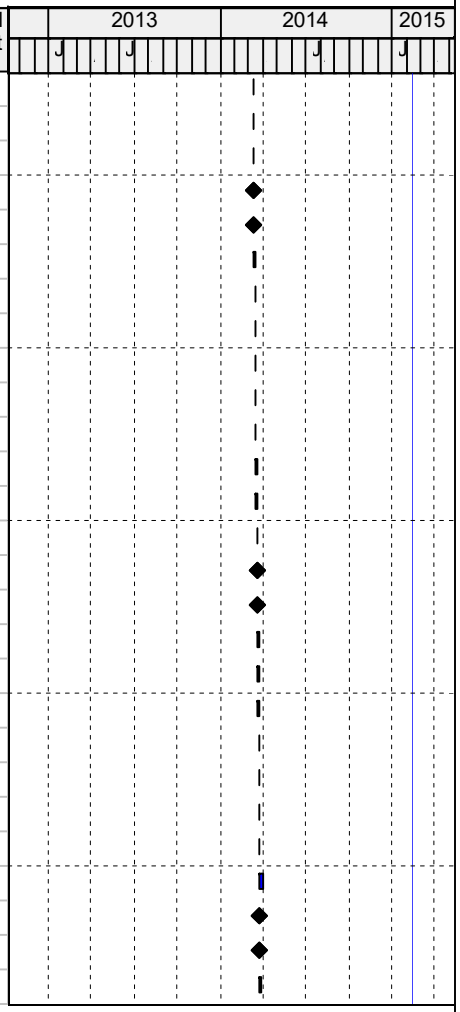



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-2018 | Remove Reshores | 2 | 0 | 26-Mar-14 A | 27-Mar-14 A | |
| P27-2004 | Shore / Form Deck | 3 | 0 | 27-Mar-14 A | 31-Mar-14 A | |
| P27-2000 | Jump/Resteel/Close Core | 4 | 0 | 29-Mar-14 A | 31-Mar-14 A | |
| P27-2006 | MEP Rough In | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2008 | ReSteel / PT Cables | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2010 | Install Edgeform/Embeds | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P26-2014 | Stress Tendons | 1 | 0 | 31-Mar-14 A | 31-Mar-14 A | |
| L09-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 31-Mar-14 A | 02-Apr-14 A | |
| P24-2016 | Strip / ReShore Deck | 3 | 0 | 01-Apr-14 A | 07-Apr-14 A | |
| L11-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 02-Apr-14 A | |
| L12-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 03-Apr-14 A | |
| P27-2012 | Place / Finish Deck | 0 | 0 | 02-Apr-14 A | | |
| P27-2020 | Place Conc @ Core | 0 | 0 | 02-Apr-14 A | | |
| P28-2002 | FRP Columns Below | 5 | 0 | 02-Apr-14 A | 04-Apr-14 A | |
| P28-2004 | Shore / Form Deck | 4 | 0 | 03-Apr-14 A | 08-Apr-14 A | |
| L10-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| P27-2014 | Stress Tendons | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| P25-2016 | Strip / ReShore Deck | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L14-2018 | Remove Reshores | 2 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| P28-2000 | Jump/Resteel/Close Core | 7 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| P28-2006 | MEP Rough In | 4 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2008 | ReSteel / PT Cables | 4 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Apr-14 A | 11-Apr-14 A | |
| L12-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| P28-2012 | Place / Finish Deck | 0 | 0 | 14-Apr-14 A | | |
| P28-2020 | Place Conc @ Core | 0 | 0 | 14-Apr-14 A | | |

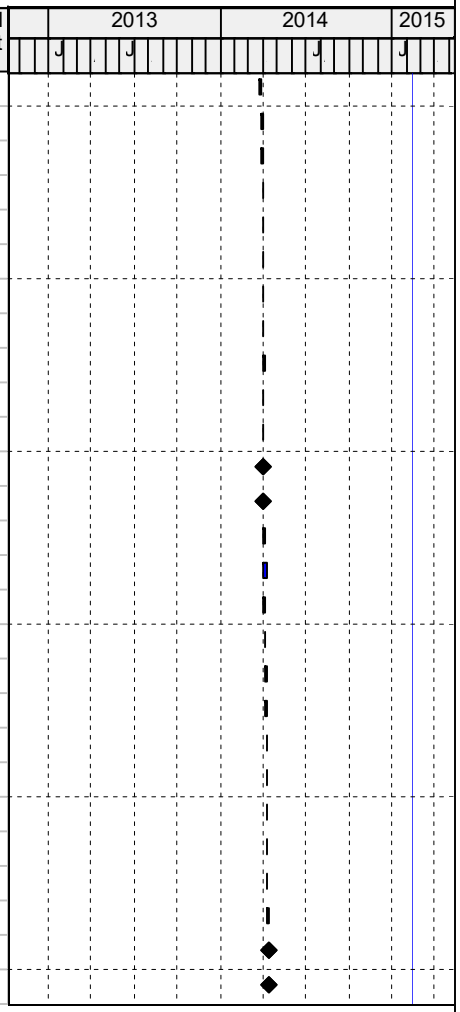


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P29-2002 | FRP Columns Above Roof Deck | 3 | 0 | 14-Apr-14 A | 18-Apr-14 A | |
| P26-2016 | Strip / ReShore Deck | 3 | 0 | 14-Apr-14 A | 17-Apr-14 A | |
| L14-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-Apr-14 A | 18-Apr-14 A | |
| P28-2014 | Stress Tendons | 1 | 0 | 17-Apr-14 A | 17-Apr-14 A | |
| P29-2000 | Strip Core | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| P27-2016 | Strip / ReShore Deck | 3 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L15-2018 | Remove Reshores | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| P28-2016 | Strip / ReShore Deck | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L15-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L16-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-May-14 A | 19-May-14 A | |
| L16-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2019 | Grind Ceiling for Skim Coat | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| **Ballroom Catwalk & Roof** | | | | | | |
| PC-2100 | Erect Structural Steel @ Porte Cochere | 3 | 0 | 30-Jan-14 A | 03-Feb-14 A | |
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 7 | 0 | 07-Feb-14 A | 17-Feb-14 A | |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| PC-2102 | Metal Decking @ Porte Cochere/ Roof | 2 | 0 | 17-Apr-14 A | 18-Apr-14 A | |
| BR-2112 | BR - Fireproofing @ Structural Steel | 2 | 0 | 27-May-14 A | 30-May-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Mech Penthouse** | | | | | | |
| PH-8706 | Set Mech Equipment @ Tower Roof | 3 | 0 | 22-May-14 A | 28-May-14 A | |
| PH-8708 | Set Equipment @ Penthouse | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| PH-8700 | PH - Structural Steel and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| **Vertical Circulation** | | | | | | |
| **Stairs** | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |

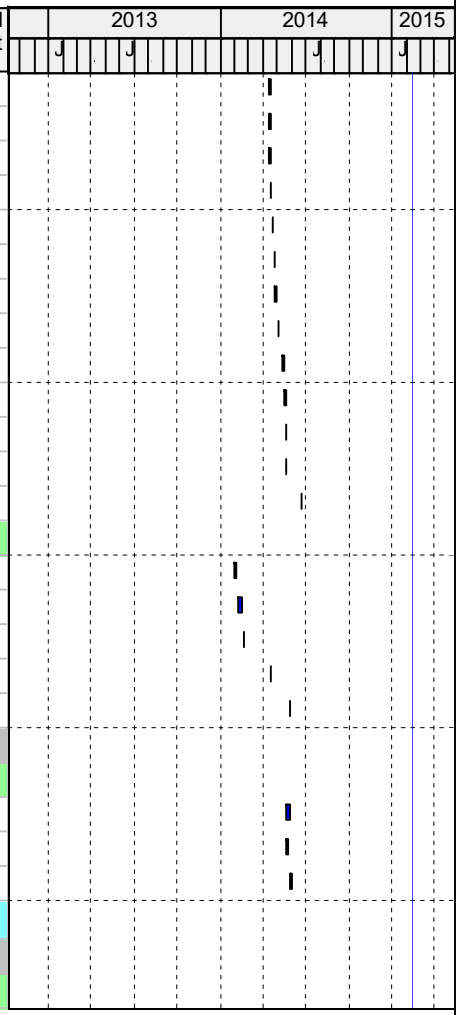



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 25-Nov-13 A | 26-Nov-13 A | |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 27-Nov-13 A | 03-Dec-13 A | |
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 04-Dec-13 A | 05-Dec-13 A | |
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 06-Dec-13 A | 09-Dec-13 A | |
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 2 | 0 | 03-Feb-14 A | 04-Feb-14 A | |
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 2 | 0 | 06-Feb-14 A | 07-Feb-14 A | |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 2 | 0 | 07-Feb-14 A | 07-Feb-14 A | |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 2 | 0 | 07-Feb-14 A | 10-Feb-14 A | |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 2 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 2 | 0 | 06-Mar-14 A | 07-Mar-14 A | |
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 2 | 0 | 07-Mar-14 A | 10-Mar-14 A | |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 2 | 0 | 13-Mar-14 A | 14-Mar-14 A | |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 2 | 0 | 08-Apr-14 A | 21-Apr-14 A | |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| S1-4040 | Stair 1 - Set Mtl Stairs / Railings L18 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 10-Dec-13 A | 11-Dec-13 A | |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 12-Dec-13 A | 13-Dec-13 A | |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 16-Dec-13 A | 17-Dec-13 A | |
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 18-Dec-13 A | 19-Dec-13 A | |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 2 | 0 | 12-Feb-14 A | 13-Feb-14 A | |

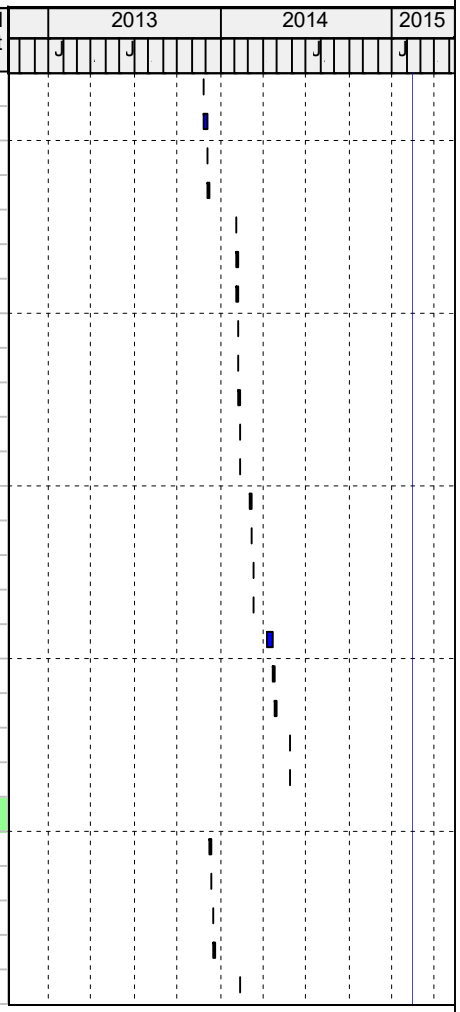



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 2 | 0 | 13-Feb-14 A | 13-Feb-14 A | |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 2 | 0 | 13-Feb-14 A | 14-Feb-14 A | |
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 2 | 0 | 19-Feb-14 A | 20-Feb-14 A | |
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 2 | 0 | 21-Feb-14 A | 24-Feb-14 A | |
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 2 | 0 | 19-Mar-14 A | 20-Mar-14 A | |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 2 | 0 | 21-Mar-14 A | 22-Mar-14 A | |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 2 | 0 | 14-May-14 A | 15-May-14 A | |
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 2 | 0 | 16-May-14 A | 19-May-14 A | |
| S2-4038 | Stair 2 - Set Mtl Stairs / Railings L17 | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - Set Metal Stairs / Railings LL2 | 6 | 0 | 05-Mar-14 A | 20-Mar-14 A | |
| S3-4002 | Stair 3 - Set Metal Stairs / Railings LL1 | 6 | 0 | 17-Mar-14 A | 21-Mar-14 A | |
| S3-4004 | Stair 3 - Permanent Railings / Final Finishes | 4 | 4 | 26-Mar-15 | 31-Mar-15 | 19 |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |
| S4-4000 | Stair 4 - Set Metal Stairs / Railings LL2 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4002 | Stair 4 - Set Metal Stairs / Railings LL1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4004 | Stair 4 -Set Metal Stairs / Railings L1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4006 | Stair 4 - Permanent Railings / Final Finishes | 4 | 4 | 25-Mar-15 | 30-Mar-15 | 18 |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |
| S6-4000 | Stair 6 - Set Metal Stairs / Railings | 5 | 0 | 25-Jun-14 A | 01-Jul-14 A | |
| S6-4002 | Stair 6 - Permanent Railings / Final Finishes | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 49 |

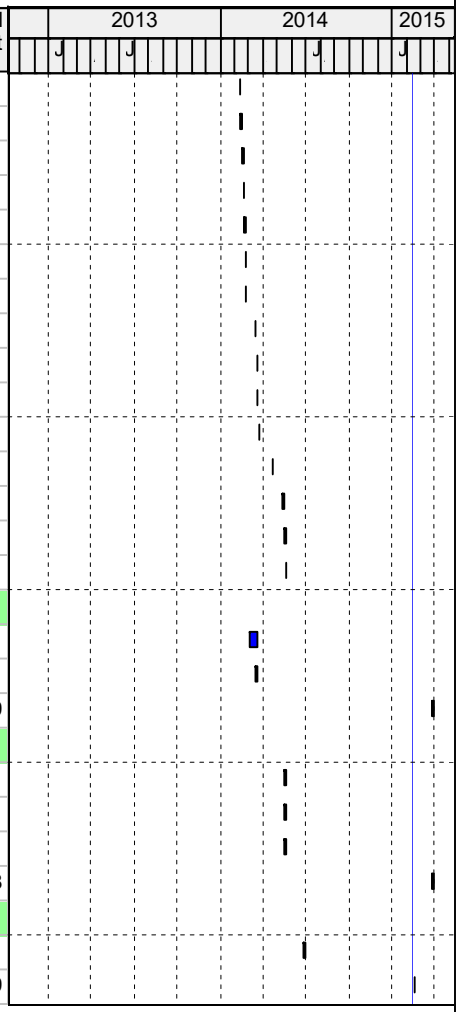



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes | 5 | 5 | 09-Apr-15 | 15-Apr-15 | 8 |
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a -Set Metal Stairs / Railings L1 | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| S4a-4002 | Stair 4a - Permanent Railings / Final Finishes | 2 | 2 | 31-Mar-15 | 01-Apr-15 | 18 |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 07-Jun-13 A | | |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 0 | 17-Jun-13 A | 21-Jun-13 A | |
| EL-1004 | Elev - Submittal Approval | 21 | 0 | 21-Jun-13 A | 01-Jan-14 A | |
| EL-1006 | Elev - Release to Manufacturing | 14 | 0 | 02-Jan-14 A | 15-Jan-14 A | |
| EL-1008 | Elev - Fabrication (Engineered Geared) | 95 | 0 | 16-Jan-14 A | 14-Jun-14 A | |
| EL-1010 | Elev - Machines delivered | 1 | 0 | 12-May-14 A | 12-May-14 A | |
| EL-1011 | Elev - Elevator Machines Flown & Set At Top Of Hoist | 5 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5016 | Elev 5 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-1216 | Elev 1&2 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-3416 | Elev 3&4 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-1202 | Elev 1&2 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-3402 | Elev 3&4 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-5018 | Elev 5 - Set Hoistway Machines | 3 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| EL-1218 | Elev 1&2 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-3418 | Elev 3&4 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-1200 | Elev 1&2 - Hoistway Clear & Ready (GC) | 0 | 0 | 20-Jun-14 A | | |

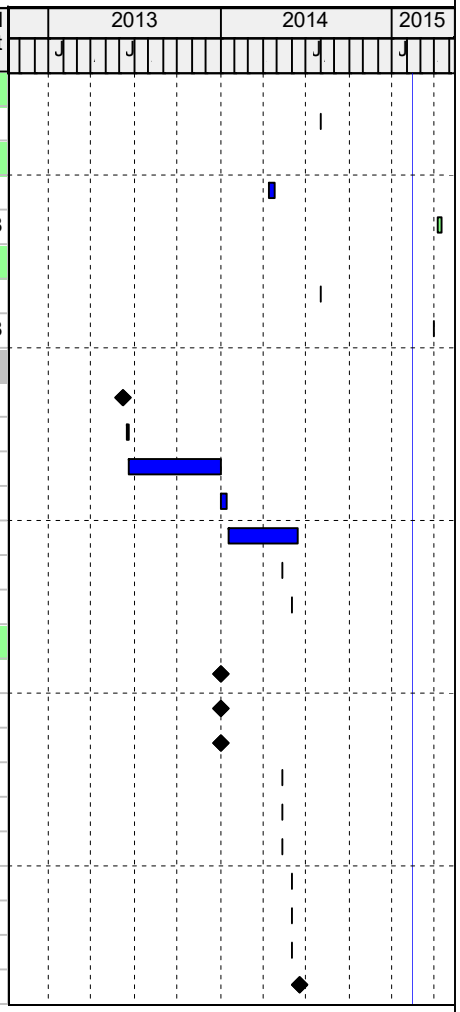


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-1204 | Elev 1&2 - Install Rails & Brackets | 17 | 0 | 23-Jun-14 A | 15-Jul-14 A | |
| EL-3400 | Elev 3&4 - Hoistway Clear & Ready (GC) | 0 | 0 | 23-Jun-14 A | | |
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 24-Jun-14 A | | |
| EL-1206 | Elev 1&2 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Jul-14 A | |
| EL-1207 | Elev 1&2 - Install Pit Equipment/Car Sling/CWT Fram | 3 | 0 | 15-Jul-14 A | 01-Aug-14 A | |
| EL-1208 | Elev 1&2 - Install MHoist & Cable | 5 | 0 | 16-Jul-14 A | 24-Jul-14 A | |
| EL-3407 | Elev 3&4 - Install Pit Equipment/Car Sling/CWT Fram | 5 | 0 | 16-Jul-14 A | 06-Aug-14 A | |
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 21-Jul-14 A | | |
| EL-5004 | Elev 5 - Install Rails & Brackets | 13 | 0 | 21-Jul-14 A | 11-Aug-14 A | |
| EL-3404 | Elev 3&4 - Install Rails & Brackets | 18 | 0 | 23-Jul-14 A | 04-Aug-14 A | |
| EL-3406 | Elev 3&4 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 28-Jul-14 A | |
| EL-3408 | Elev 3&4 - Install Hoist & Cable | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| EL-5007 | Elev 5 - Install Pit Equipment/Car Sling/CWT Frame/V | 5 | 0 | 12-Aug-14 A | 15-Aug-14 A | |
| EL-1210 | Elev 1&2 - Install Entrances/Doors/Fixtures/Fascia | 19 | 0 | 14-Aug-14 A | 22-Sep-14 A | |
| EL-3410 | Elev 3&4 - Install Entrances/Doors/Fixtures/Fascia | 30 | 0 | 14-Aug-14 A | 02-Oct-14 A | |
| EL-5006 | Elev 5 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Aug-14 A | |
| EL-5008 | Elev 5 - Install MHoist & Cable | 4 | 0 | 18-Aug-14 A | 20-Aug-14 A | |
| EL-5010 | Elev 5 - Install Entrances/Doors/Fixtures/Fascia | 21 | 0 | 21-Aug-14 A | 26-Sep-14 A | |
| EL-1212 | Elev 1&2 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 22-Sep-14 A | 13-Oct-14 A | |
| EL-5012 | Elev 5 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 26-Sep-14 A | 16-Oct-14 A | |
| EL-3412 | Elev 3&4 - Install Hoistway Equipment/Pipe & Wire | 23 | 0 | 03-Oct-14 A | 03-Nov-14 A | |
| EL-1214 | Elev 1&2 - Install Cab/Wiring/Door Operator(s) | 11 | 0 | 14-Oct-14 A | 28-Oct-14 A | |
| EL-5014 | Elev 5 - Install Cab/Wiring/Door Operator(s) | 7 | 0 | 17-Oct-14 A | 27-Oct-14 A | |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 1 | 0 | 24-Oct-14 A | 24-Oct-14 A | |
| EL-6016 | Elev 6 - Hoistway Walls Complete (GC) | 0 | 0 | | 24-Oct-14 A | |
| EL-6004 | Elev 6 - Install Cylinders/Rails & Brackets | 4 | 0 | 27-Oct-14 A | 30-Oct-14 A | |
| EL-5022 | Elev 5 - Adjust | 5 | 0 | 28-Oct-14 A | 03-Nov-14 A | |

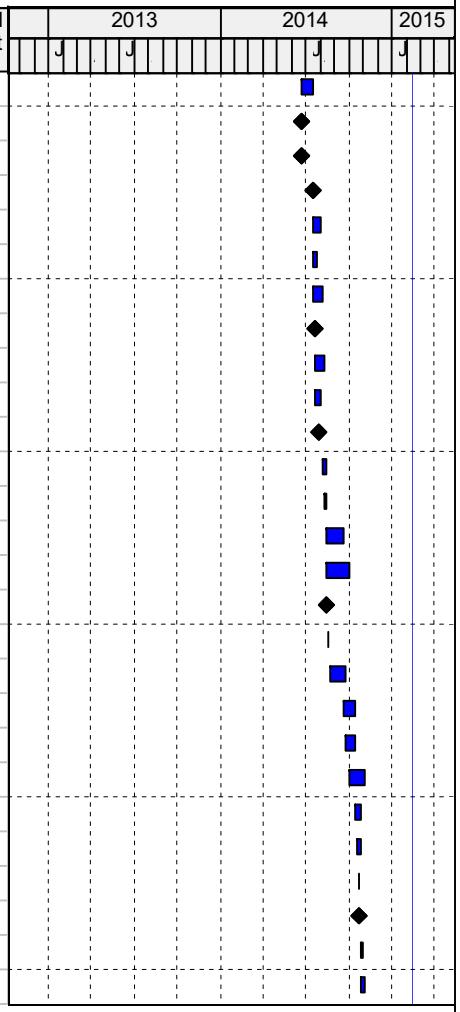



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-1222 | Elev 1&2 - Adjust | 5 | 0 | 29-Oct-14 A | 04-Nov-14 A | |
| EL-6006 | Elev 6 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 30-Oct-14 A | |
| EL-6007 | Elev 6 - Install Pit Equipment/Car Sling | 2 | 0 | 31-Oct-14 A | 03-Nov-14 A | |
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| EL-3414 | Elev 3&4 - Install Cab/Wiring/Door Operator(s) | 10 | 0 | 04-Nov-14 A | 17-Nov-14 A | |
| EL-6018 | Elev 6 - Install Machine Room Equipment | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| EL-1224 | Elev 1&2 - Clean / Paint / Punchlist | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| EL-5026 | Elev 5 - Inspections | 7 | 0 | 13-Nov-14 A | 14-Nov-14 A | |
| EL-3422 | Elev 3&4 - Adjust | 8 | 0 | 18-Nov-14 A | 20-Nov-14 A | |
| EL-6012 | Elev 6 - Install hoistway rails & divider beams | 2 | 0 | 20-Nov-14 A | 21-Nov-14 A | |
| EL-6010 | Elev 6 - Install elevator fronts/rears | 9 | 0 | 09-Dec-14 A | 24-Dec-14 A | |
| EL-6014 | Elev 6 - Cab build-out | 5 | 0 | 15-Dec-14 A | 30-Jan-15 A | |
| EL-1226 | Elev 1&2 - CoB/L&I Inspections | 2 | 2 | 17-Feb-15 | 18-Feb-15 | 20 |
| EL-6022 | Elev 6 - Final cleaning at EMR | 4 | 4 | 20-Feb-15 | 25-Feb-15 | 30 |
| EL-3424 | Elev 3&4 - Walsh/TKE pre-inspection | 6 | 6 | 10-Mar-15* | 17-Mar-15 | 18 |
| EL-6024 | Elev 6 - Walsh/TKE pre-inspection | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 18 |
| EL-3426 | Elev 3&4 - CoB/L&I Inspections | 3 | 3 | 18-Mar-15 | 20-Mar-15 | 18 |
| EL-6026 | Elev 6 - CoB/L&I Inspections | 1 | 1 | 18-Mar-15 | 18-Mar-15 | 18 |
| **Exterior Shell** | | | | | | |
| Elevations | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2** | | | | | | |
| L3D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Feb-14 A | 12-Feb-14 A | |
| L3-5308 | L3- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 17-Feb-14 A | 21-Feb-14 A | |
| L4D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Feb-14 A | 19-Feb-14 A | |
| L4-5308 | L4- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Feb-14 A | 28-Feb-14 A | |
| L5D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Feb-14 A | 26-Feb-14 A | |

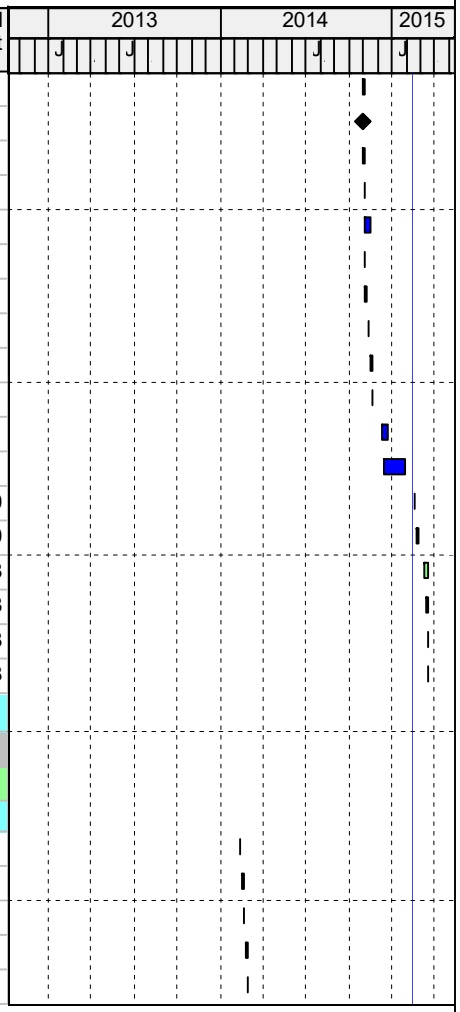



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L5-5308 | L5- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 03-Mar-14 A | 07-Mar-14 A | |
| L6D5308 | Deliver/Stock Wall Panels | 1 | 0 | 05-Mar-14 A | 05-Mar-14 A | |
| L6-5308 | L6- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L7-5308 | L7- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L7D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Mar-14 A | 12-Mar-14 A | |
| L8D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Mar-14 A | 19-Mar-14 A | |
| L8-5308 | L8- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Mar-14 A | 28-Mar-14 A | |
| L9D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L9-5308 | L9- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 31-Mar-14 A | 07-Apr-14 A | |
| 10D5308 | Deliver/Stock Wall Panels | 1 | 0 | 02-Apr-14 A | 02-Apr-14 A | |
| L10-5308 | L10- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 07-Apr-14 A | 11-Apr-14 A | |
| 11D5308 | Deliver/Stock Wall Panels | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L11-5308 | L11- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 11-Apr-14 A | 18-Apr-14 A | |
| 12D5308 | Deliver/Stock Wall Panels | 1 | 0 | 16-Apr-14 A | 16-Apr-14 A | |
| L12-5308 | L12- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Apr-14 A | 25-Apr-14 A | |
| 14D5308 | Deliver/Stock Wall Panels | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L14-5308 | L14 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Apr-14 A | 01-May-14 A | |
| 15D5308 | Deliver/Stock Wall Panels | 1 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L15-5308 | L15 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| 16D5308 | Deliver/Stock Wall Panels | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L16-5308 | L16- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| 17D5308 | Deliver/Stock Wall Panels | 1 | 0 | 14-May-14 A | 14-May-14 A | |
| L17-5308 | L17 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 20-May-14 A | 11-Jun-14 A | |
| LL2-5308 | LL2 Thru L4 - Support Frame/Sheathing for Metal Wa | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL1-5308 | LL1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| L1-5308 | L1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| **Level 1** | | | | | | |

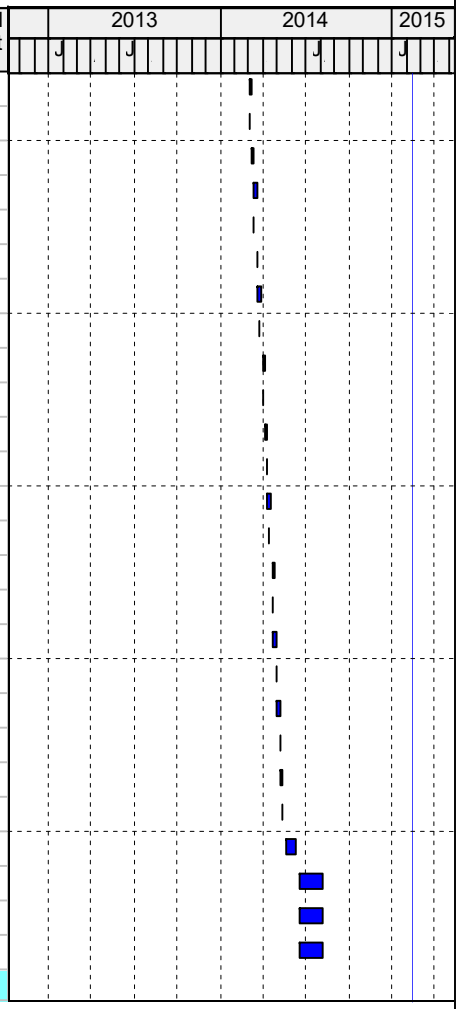



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L3-5102 | L3- Storefront Frames | 7 | 0 | 18-Aug-14 A | 29-Sep-14 A | |
| L1-5102 | L1 - Storefront Frames (excl. Main Entry Facade) | 8 | 0 | 02-Sep-14 A | 11-Sep-14 A | |
| L1-5104 | L1 - Storefront Glazing (excl. Main Entry Facade) | 4 | 0 | 19-Sep-14 A | 24-Sep-14 A | |
| EP-5110 | L1 - Revolving Doors | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L3-5104 | L3 - Storefront Glazing | 3 | 0 | 30-Sep-14 A | 03-Oct-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Levels 3-4** | | | | | | |
| L3-5130 | L3 - Install Punch Windows | 5 | 0 | 24-Feb-14 A | 10-Mar-14 A | |
| L4-5130 | L4 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 12-Mar-14 A | |
| L5-5130 | L5 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L6-5130 | L6- Install Punch Windows | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L7-5130 | L7 - Install Punch Windows | 5 | 0 | 18-Mar-14 A | 21-Mar-14 A | |
| L8-5130 | L8 - Install Punch Windows | 5 | 0 | 24-Mar-14 A | 28-Mar-14 A | |
| L9-5130 | L9 - Install Punch Windows | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L10-5130 | L10 - Install Punch Windows | 5 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-5130 | L11 - Install Punch Windows | 5 | 0 | 14-Apr-14 A | 21-Apr-14 A | |
| L12-5130 | L12 - Install Punch Windows | 5 | 0 | 22-Apr-14 A | 25-Apr-14 A | |
| L14-5130 | L14 - Install Punch Windows | 5 | 0 | 28-Apr-14 A | 05-May-14 A | |
| L15-5130 | L15 - Install Punch Windows | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| L16-5130 | L16 - Install Punch Windows | 5 | 0 | 12-May-14 A | 20-May-14 A | |
| L17-5130 | L17 - Install Punch Windows | 5 | 0 | 27-May-14 A | 16-Jun-14 A | |
| **Roofs** | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| RF-4026 | L1 - City Park - Protection Board | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| **Pool Membrane - (elev 18')** | | | | | | |

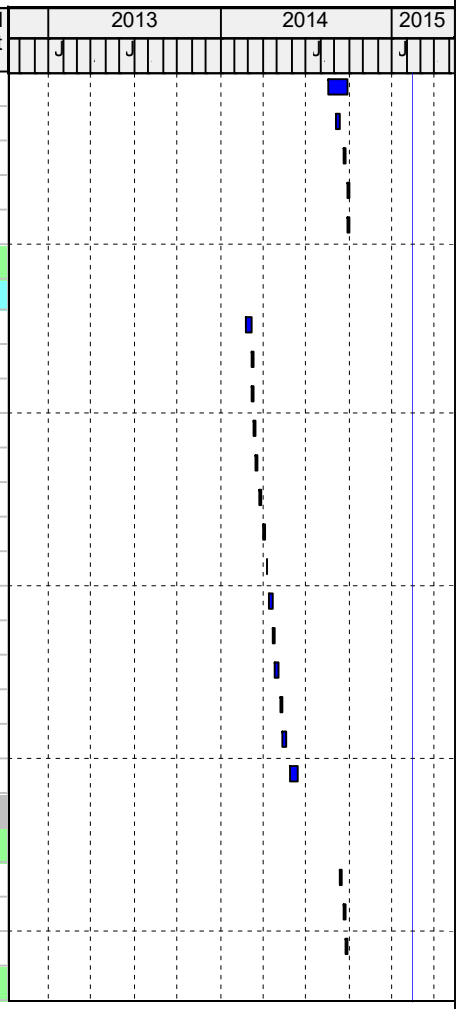



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| RF-4034 | Pool - Install plumbing | 3 | 0 | 20-Oct-14 A | 22-Oct-14 A | |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |
| RF-4010 | AR - Set Mechanical Equipment | 5 | 0 | 10-Jun-14 A | 12-Jun-14 A | |
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 10 | 0 | 04-Aug-14 A | 27-Aug-14 A | |
| RF-4012 | L2.5 Horseshoe - Install corrugated metal panels | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 8 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |
| PC-4008 | RF - Entry / Porte Cochere Roofing System | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | RF - Upper Ballroom Roofing System | 3 | 0 | 28-Jul-14 A | 31-Jul-14 A | |
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 4 | 0 | 31-Jul-14 A | 04-Aug-14 A | |
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |
| RF-4018 | TR - Terrace Roof - Green Roofing System | 5 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| RF-4020 | TR - Terrace Roof - Install sheet metal capping[DELE | 1 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4022 | TR - Terrace Roof - Install deocrative metal railing | 3 | 3 | 23-Feb-15 | 25-Feb-15 | 35 |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Perimeter Framing / Sul | 10 | 0 | 02-Jun-14 A | 08-Jul-14 A | |
| RF-4002 | Tower Roof - Roofing System | 10 | 0 | 20-Aug-14 A | 17-Sep-14 A | |
| **PH - Roof - (elev 173')** | | | | | | |
| RF-4030 | PH - Roofing System | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| RF-4032 | PH - Coping / Flashing [DELETED] | 3 | 0 | 01-Sep-14 A | 01-Sep-14 A | |
| **Rough-In's** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6002 | LL4 - Layout | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |

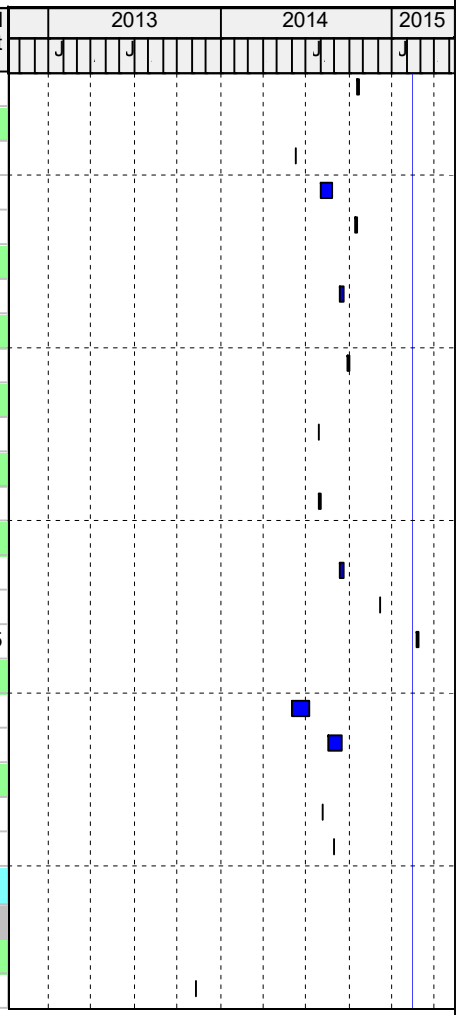



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-6008 | LL4 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL4-6012 | LL4 - Fire Sprinkler RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6014 | LL4 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6018 | LL4 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6004 | LL4 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL4-6016 | LL4 - Electrical RI | 10 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties RI | 8 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6010 | LL4 - Elevator pits | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| LL4-6020 | LL4 - H Mtl Frames | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL4-6024 | LL4 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6002 | LL3 - Layout | 1 | 0 | 19-Nov-13 A | 19-Nov-13 A | |
| LL3-6008 | LL3 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL3-6012 | LL3 - Fire Sprinkler RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6014 | LL3 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6018 | LL3 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6004 | LL3 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL3-6020 | LL3 - H Mtl Frames | 3 | 0 | 08-May-14 A | 09-May-14 A | |
| LL3-6010 | LL3 - F/P Curbs | 5 | 0 | 19-May-14 A | 19-May-14 A | |
| LL3-6016 | LL3 - Electrical RI | 2 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties RI | 8 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL3-6024 | LL3 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6002 | LL2 - Layout | 1 | 0 | 14-Jan-14 A | 14-Jan-14 A | |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |

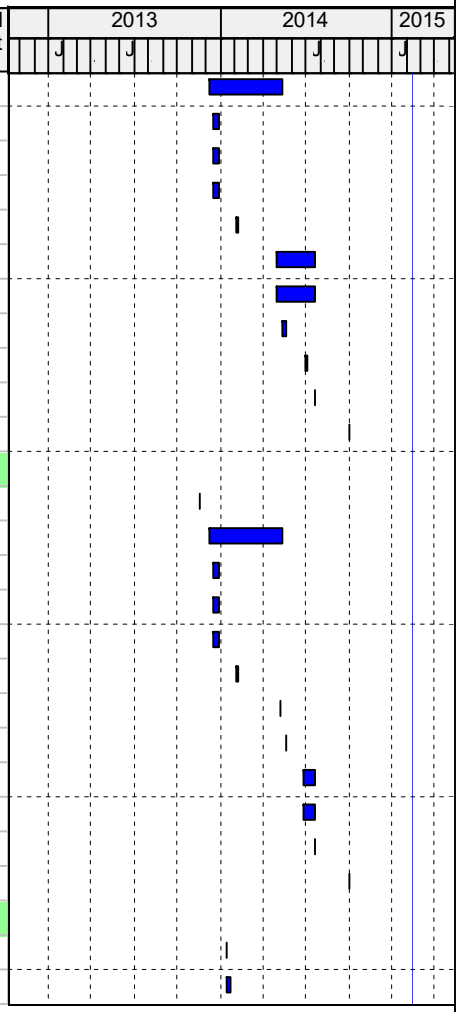


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-6012 | LL2 - Fire Sprinkler RI | 10 | 0 | 21-Jan-14 A | 03-Feb-14 A | |
| LL2-6014 | LL2 - Plumbing RI | 10 | 0 | 21-Jan-14 A | 14-Feb-14 A | |
| LL2E-6016 | LL2 - Electrical RI | 8 | 0 | 03-Feb-14 A | 17-Mar-14 A | |
| LL2-6016 | LL2 - Electrical RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2-6018 | LL2 - HVAC RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2–6004 | LL2 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL2E-6004 | LL2 - CMU Walls | 10 | 0 | 04-Mar-14 A | 09-May-14 A | |
| LL2E-6012 | LL2 - Fire Sprinkler RI | 8 | 0 | 21-Mar-14 A | 01-Apr-14 A | |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 24-Apr-14 A | |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 3 | 0 | 23-Apr-14 A | 21-Jul-14 A | |
| LL2E-6020 | LL2 - H Mtl Frames | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| LL2-6020 | LL2 - H Mtl Frames | 3 | 0 | 12-May-14 A | 13-May-14 A | |
| LL2E-6008 | LL2 - Int Wall Framing | 5 | 0 | 13-May-14 A | 22-Jun-14 A | |
| LL2E-6014 | LL2 - Plumbing RI | 8 | 0 | 13-May-14 A | 30-May-14 A | |
| LL2E-6018 | LL2 - HVAC RI | 8 | 0 | 13-May-14 A | 04-Aug-14 A | |
| LL2E-6022 | LL2 - Fire Alarm / Elec Specialties RI (East of 10) | 8 | 0 | 13-May-14 A | 22-Sep-14 A | |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties RI (West of 10) | 8 | 0 | 19-May-14 A | 22-Sep-14 A | |
| LL2-6015 | LL2 - Main Elect Room Set Equip / RI - Power to Ma | 15 | 0 | 30-Jun-14 A | 26-Sep-14 A | |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 0 | 16-Jul-14 A | 21-Jul-14 A | |
| LL2-6024 | LL2 - Inspections | 2 | 0 | 15-Sep-14 A | 03-Oct-14 A | |
| LL2-6010 | F/P Curbs at Garage | 5 | 5 | 30-Mar-15 | 03-Apr-15 | 11 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6002 | Layout | 3 | 0 | 03-Jan-14 A | 08-Jan-14 A | |
| LL1-6008 | Int Wall Framing & Inspection | 6 | 0 | 08-Jan-14 A | 21-Jul-14 A | |
| LL1-Z2-6002 | Layout | 3 | 0 | 08-Jan-14 A | 14-Jan-14 A | |
| LL1-Z3-6002 | Layout | 3 | 0 | 14-Jan-14 A | 17-Jan-14 A | |

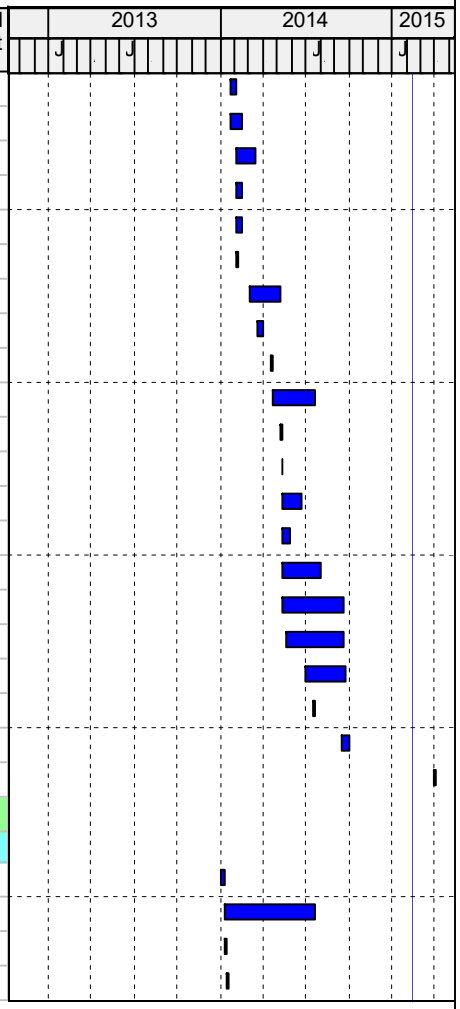


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-6008 | Int Wall Framing & Inspection | 6 | 0 | 17-Jan-14 A | 01-Aug-14 A | |
| LL1-Z3-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-Jan-14 A | 04-Aug-14 A | |
| LL1-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 09-May-14 A | |
| LL1-Z2-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 28-Apr-14 A | |
| LL1-Z3-6004 | CMU Walls (At All Areas North of Q-Line) | 3 | 0 | 03-Feb-14 A | 13-May-14 A | |
| LL1C-6012 | Complete Fire Sprinkler RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6016 | Complete Electrical RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 10 | 0 | 17-Feb-14 A | 16-Sep-14 A | |
| LL1C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 30-Apr-14 A | |
| LL1-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-Z2-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z2-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z3-6012 | Fire Sprinkler RI (At All Areas North of Q-Line) | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z3-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 11-Sep-14 A | |
| LL1-Z3-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z2C-6012 | Complete Fire Sprinkler RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6014 | Complete Plumbing RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6016 | Complete Electrical RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |

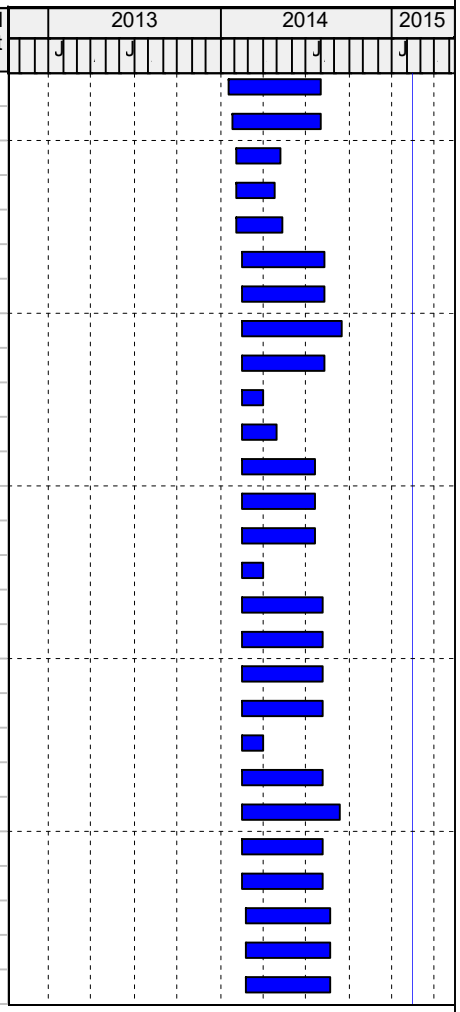



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 15 | 0 | 24-Feb-14 A | 15-Sep-14 A | |
| LL1-Z2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2-6020 | Hollow Metal Door Frames | 5 | 0 | 17-Mar-14 A | 04-Apr-14 A | |
| LL1-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| LL1-Z3-6020 | Hollow Metal Door Frames (At All Areas North of Q-Lir | 1 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| L1B-6004 | CMU Walls [including East Service Corridor] | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L1L-6002 | Layout [including back of house] | 3 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 29-Apr-14 A | |
| L1B-6008 | Int Wall Framing & Inspection | 6 | 0 | 21-Apr-14 A | 08-Aug-14 A | |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 5 | 0 | 25-Apr-14 A | 21-Jul-14 A | |
| LL1C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L1K-6004 | CMU Walls [including public restroom] | 3 | 0 | 05-May-14 A | 08-May-14 A | |
| L1K-6002 | Layout [including public restroom] | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| L1K-6008 | Int Wall Framing & Inspection | 4 | 0 | 09-May-14 A | 22-Aug-14 A | |
| L1B-6002 | Layout [including East Service Corridor] | 3 | 0 | 14-May-14 A | 27-May-14 A | |
| L1L-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-May-14 A | 06-Oct-14 A | |
| L1L-6004 | CMU Walls [including back of house] | 3 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L1K-6012 | Fire Sprinkler RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6014 | Plumbing RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6016 | Electrical RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1K-6018 | HVAC RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1B-6014 | Plumbing RI [including East Service Corridor] | 10 | 0 | 16-Jun-14 A | 24-Jun-14 A | |
| L1B-6018 | HVAC RI | 10 | 0 | 20-Jun-14 A | 15-Aug-14 A | |
| L1B-6012 | Fire Sprinkler RI | 10 | 0 | 21-Jun-14 A | 15-Aug-14 A | |
| L1L-6018 | HVAC RI | 5 | 0 | 23-Jun-14 A | 13-Oct-14 A | |
| L1L-6014 | Plumbing RI | 5 | 0 | 24-Jun-14 A | 28-Oct-14 A | |
| L1L-6010 | CMU Seismic Clips [including back of house] [DELET | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |

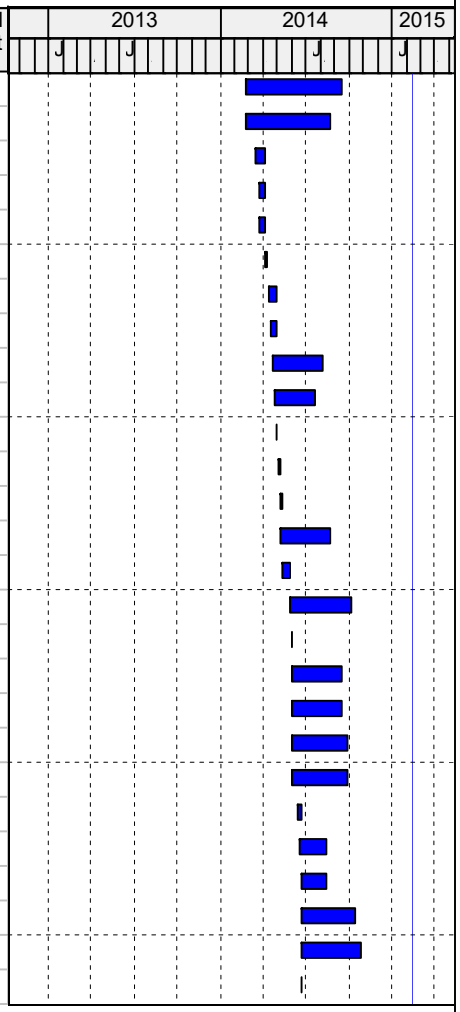


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-6012 | Fire Sprinkler RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |
| L1L-6016 | Electrical RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |
| L1L-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 27-Jun-14 A | 13-Oct-14 A | |
| L1K-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 27-Jun-14 A | 29-Sep-14 A | |
| LL1-Z3-6009 | Frame Ceilings [DELETED] | 4 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1B-6016 | Electrical RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| L1B-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| LL1-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-Z2-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L1B-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-6024 | Inspections for Cover | 1 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L1B-6020 | Hollow Metal Door Frames | 5 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| LL1-Z3-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L1K-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 06-Aug-14 A | |
| LL1-Z2-6024 | Inspections for Cover | 2 | 0 | 07-Aug-14 A | 08-Aug-14 A | |
| L1K-6020 | Hollow Metal Door Frames | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-Z2-6009 | Frame Ceilings & Inspection | 6 | 0 | 22-Aug-14 A | 13-Oct-14 A | |
| L1L-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Aug-14 A | 13-Oct-14 A | |
| LL1-6009 | Frame Ceilings & Inspection (except for bar redesign | 9 | 0 | 02-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3-6024 | Inspections for Cover | 2 | 0 | 12-Sep-14 A | 12-Sep-14 A | |
| LL1-Z3C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6016 | Complete Electrical RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3C-6018 | Complete HVAC RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| L1KC-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 4 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L1B-6024 | Inspections for Cover (Main Ballroom N/S/W Walls & | 3 | 0 | 02-Oct-14 A | 03-Oct-14 A | |

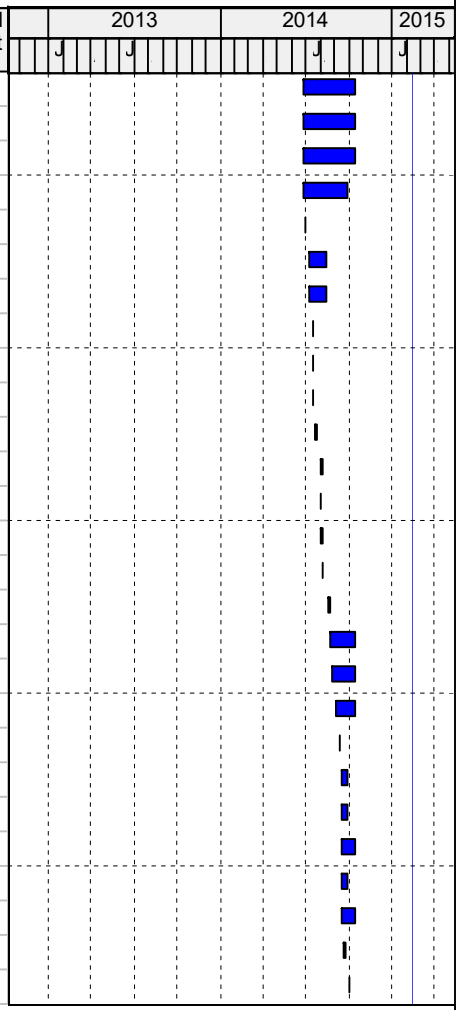


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-6024 | Inspections for Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1KC-6014 | Complete Plumbing RI @ Ceilings & Inspection | 4 | 0 | 02-Oct-14 A | 07-Oct-14 A | |
| L1BC-6014 | Complete Plumbing RI @ Ceilings | 7 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L1KC-6018 | Complete HVAC RI @ Ceilings & Inspection | 4 | 0 | 06-Oct-14 A | 10-Nov-14 A | |
| L1KC-6016 | Complete Electrical RI @ Ceilings & Inspection | 3 | 0 | 20-Oct-14 A | 10-Nov-14 A | |
| L1KC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 3 | 0 | 20-Oct-14 A | 10-Nov-14 A | |
| L1L-6024 | Inspections for Cover | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L1L-6009 | Frame ceilings & inspection at high ceiling | 13 | 0 | 24-Nov-14 A | 20-Jan-15 A | |
| L1B-6009 | Frame Ceilings & inspection at Main Ballroom (per rev | 5 | 0 | 04-Dec-14 A | 16-Jan-15 A | |
| L1LC-6012 | Complete fire sprinkler RI @ ceilings | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1LC-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| L1LC-6016 | Complete electrical rough-in @ ceilings & inspection | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1LC-6018 | Complete HVAC RI @ Ceilings | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1LC-6022 | Complete fire alarm/elec specialties RI @ ceilings & ir | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1K-6009 | Frame ceilings & inspection at public restroom | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L1B-8118 | Lighting & electrical trim at Ballrooms | 5 | 5 | 25-Mar-15 | 31-Mar-15 | 0 |
| L1B-8204 | HVAC trim at Ballrooms | 5 | 5 | 25-Mar-15 | 31-Mar-15 | 0 |
| L1B-8112 | Fire sprinkler trim at Ballrooms | 2 | 2 | 27-Mar-15 | 30-Mar-15 | 3 |
| L1BC-6022 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 27-Mar-15 | 30-Mar-15 | 3 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 0 | 17-Apr-14 A | 09-May-14 A | |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6006 | L2 - Support Frame/Sheathing for Metal Panels | 6 | 0 | 23-Apr-14 A | 07-Aug-14 A | |
| L02-6008 | L2 - Int Wall Framing | 10 | 0 | 25-Apr-14 A | 17-Jul-14 A | |
| L02-6014 | L2 - Plumbing RI | 15 | 0 | 28-Apr-14 A | 07-Aug-14 A | |
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 0 | 28-Apr-14 A | 09-May-14 A | |
| L02-6004 | L2 - CMU Walls | 5 | 0 | 29-Apr-14 A | 12-May-14 A | |

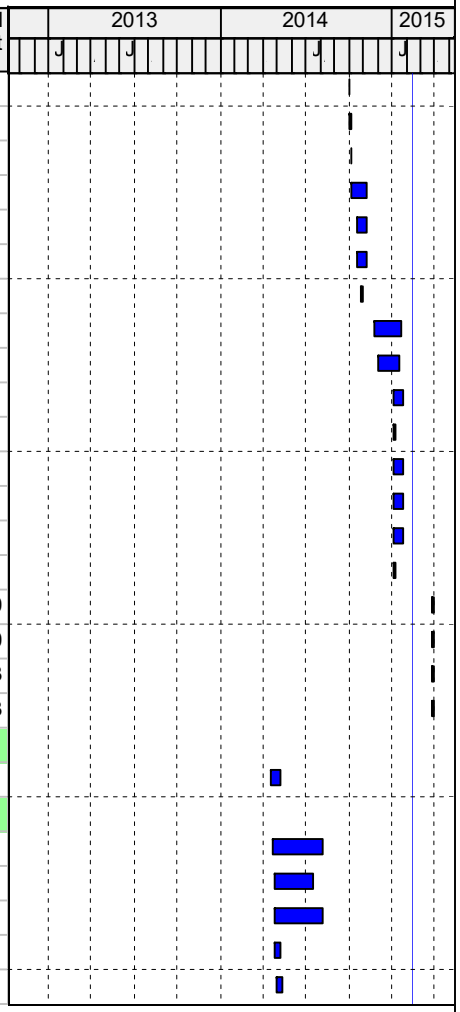


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-6002 | L2 - Layout | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L02-6018 | L2 - HVAC Rl (including equipment) | 20 | 0 | 18-Jun-14 A | 10-Sep-14 A | |
| L02-6016 | L2 - Electrical Rl | 10 | 0 | 24-Jun-14 A | 14-Aug-14 A | |
| L02-6022 | L2 - Fire Alarm / Elec Specialties Rl | 10 | 0 | 24-Jun-14 A | 10-Oct-14 A | |
| L02-6012 | L2 - Fire Sprinkler Rl | 10 | 0 | 26-Jun-14 A | 07-Aug-14 A | |
| L02-6020 | L2 - H Mtl Frames | 5 | 0 | 11-Jul-14 A | 17-Jul-14 A | |
| L02-6024 | L2 - Inspections - North Half | 2 | 0 | 10-Oct-14 A | 20-Oct-14 A | |
| Upper Tower - (Levels 3 thru PH) | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L07-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 01-Apr-11 A | 11-Apr-11 A | |
| L04-6012 | Fire Sprinkler Mains | 5 | 0 | 01-Feb-14 A | 03-Apr-14 A | |
| L03-8219 | HVAC Risers | 5 | 0 | 11-Feb-14 A | 23-Mar-14 A | |
| L03-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 11-Feb-14 A | 03-Mar-14 A | |
| L03-6002 | Layout | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| L04-8219 | HVAC Risers | 5 | 0 | 13-Feb-14 A | 23-Mar-14 A | |
| L05-8219 | HVAC Risers | 5 | 0 | 17-Feb-14 A | 03-Mar-14 A | |
| L03-6008 | Frame Shaft Walls | 3 | 0 | 18-Feb-14 A | 26-Mar-14 A | |
| L04-6002 | Layout | 5 | 0 | 19-Feb-14 A | 25-Feb-14 A | |
| L04-6008 | Frame Shaft Walls | 3 | 0 | 20-Feb-14 A | 26-Mar-14 A | |
| L03-6011 | PreRock Shafts | 2 | 0 | 24-Feb-14 A | 25-Mar-14 A | |
| L03-6010 | Frame Walls | 5 | 0 | 25-Feb-14 A | 25-Mar-14 A | |
| L05-6002 | Layout | 5 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| L04-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 28-Feb-14 A | 05-Mar-14 A | |
| L03-6016 | Electrical Rl | 5 | 0 | 03-Mar-14 A | 04-Apr-14 A | |
| L03-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 12-Mar-14 A | |
| L04-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 13-Mar-14 A | |

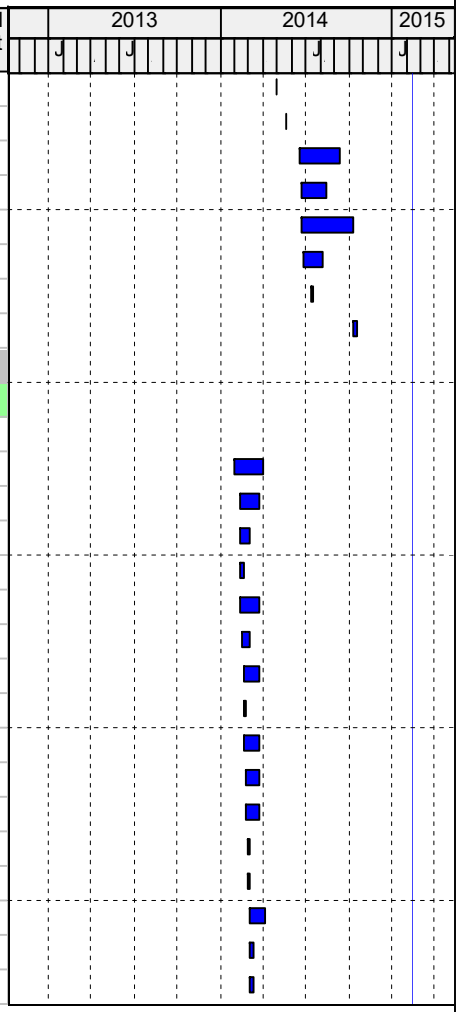


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6010 | Frame Walls | 5 | 0 | 04-Mar-14 A | 05-Jun-14 A | |
| L05-6008 | Frame Shaft Walls | 3 | 0 | 05-Mar-14 A | 27-Mar-14 A | |
| L06-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L07-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L05-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 06-Mar-14 A | 21-Mar-14 A | |
| L03-6020 | Install Hollow Metal Frames | 3 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L04-6020 | Install Hollow Metal Frames | 3 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L05-6010 | Frame Walls | 5 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L06-6002 | Layout | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L04-6011 | PreRock Shafts | 2 | 0 | 18-Mar-14 A | 25-Mar-14 A | |
| L05-6009 | Inspect Shafts | 1 | 0 | 18-Mar-14 A | 18-Mar-14 A | |
| L05-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| L06-6008 | Frame Shaft Walls | 3 | 0 | 19-Mar-14 A | 03-Apr-14 A | |
| L06-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 27-Mar-14 A | |
| L04-6016 | Electrical RI | 5 | 0 | 20-Mar-14 A | 09-Apr-14 A | |
| L05-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 26-Mar-14 A | |
| L06-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 07-Apr-14 A | |
| L07-6002 | Layout | 5 | 0 | 24-Mar-14 A | 30-Apr-14 A | |
| L03-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L03-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L05-6016 | Electrical RI | 5 | 0 | 25-Mar-14 A | 05-Jun-14 A | |
| L04-6019 | Complete Top Out GWB | 2 | 0 | 26-Mar-14 A | 06-Jun-14 A | |
| L05-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L06-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| L03-6019 | Complete Top Out GWB | 2 | 0 | 27-Mar-14 A | 02-May-14 A | |

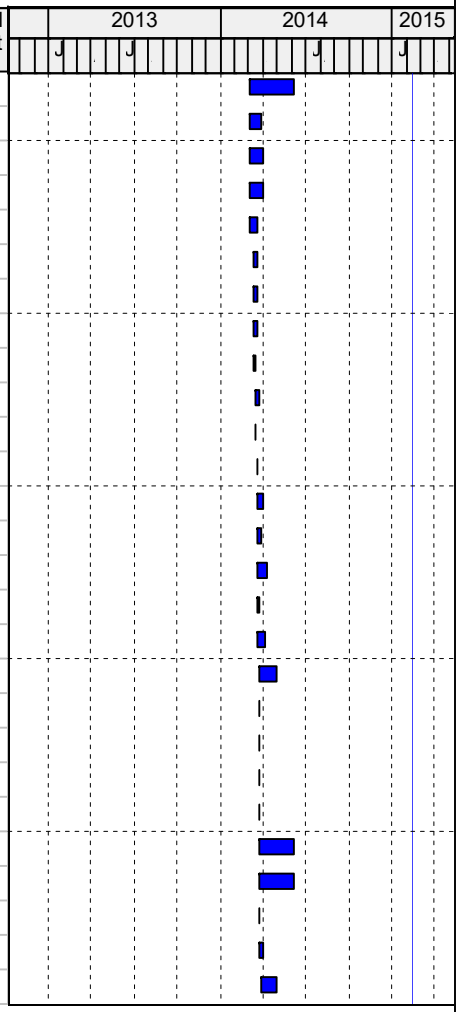


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-6002 | Layout | 5 | 0 | 27-Mar-14 A | 02-Apr-14 A | |
| L05-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 28-Mar-14 A | 03-Apr-14 A | |
| L06-6010 | Frame Walls | 5 | 0 | 28-Mar-14 A | 07-Apr-14 A | |
| L03-6012 | Fire Sprinkler Mains | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L07-6008 | Frame Shaft Walls | 3 | 0 | 31-Mar-14 A | 03-Apr-14 A | |
| L05-6019 | Complete Top Out GWB | 2 | 0 | 01-Apr-14 A | 08-Apr-14 A | |
| L08-6008 | Frame Shaft Walls | 3 | 0 | 02-Apr-14 A | 21-Apr-14 A | |
| L03-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L04-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L05-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L06-6016 | Electrical RI | 5 | 0 | 03-Apr-14 A | 15-Apr-14 A | |
| L07-6009 | Inspect Shafts | 1 | 0 | 03-Apr-14 A | 03-Apr-14 A | |
| L07-6011 | PreRock Shafts | 2 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| L05-6012 | Fire Sprinkler Mains | 5 | 0 | 04-Apr-14 A | 30-Apr-14 A | |
| L06-6012 | Fire Sprinkler Mains | 5 | 0 | 07-Apr-14 A | 30-Apr-14 A | |
| L06-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L06-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L07-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| L07-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L03-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L03-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L04-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L06-6009 | Inspect Shafts | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L06-6019 | Complete Top Out GWB | 2 | 0 | 08-Apr-14 A | 18-Apr-14 A | |
| L07-6010 | Frame Walls | 5 | 0 | 08-Apr-14 A | 15-Apr-14 A | |
| L08-6011 | PreRock Shafts | 2 | 0 | 08-Apr-14 A | 23-Apr-14 A | |
| L09-6002 | Layout | 5 | 0 | 08-Apr-14 A | 26-Apr-14 A | |

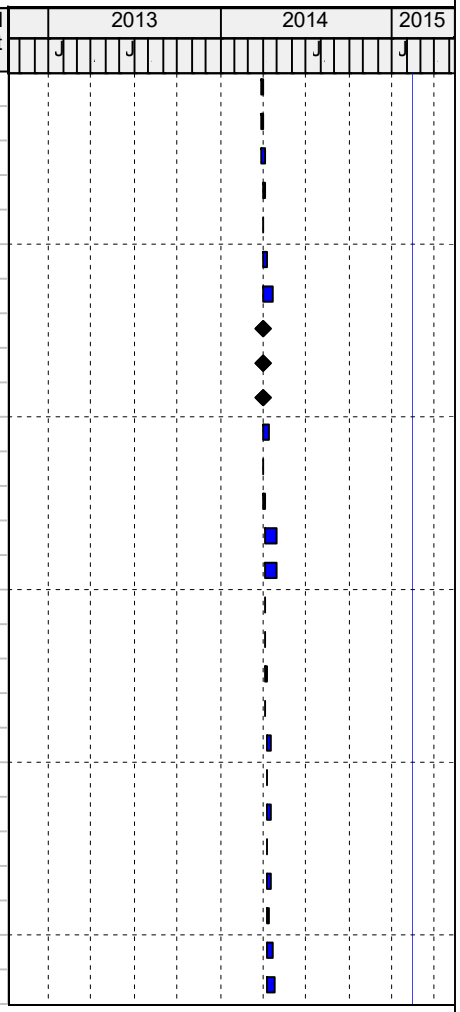


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 09-Apr-14 A | 08-May-14 A | |
| L03-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L05-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 09-Apr-14 A | 14-Apr-14 A | |
| L08-6009 | Inspect Shafts | 1 | 0 | 09-Apr-14 A | 25-Apr-14 A | |
| L09-6008 | Frame Shaft Walls | 3 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| L08-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| L04-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 15-Apr-14 A | 16-Apr-14 A | |
| L07-6012 | Fire Sprinkler Mains | 5 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| L07-6016 | Electrical RI | 5 | 0 | 15-Apr-14 A | 12-May-14 A | |
| L07-6020 | Install Hollow Metal Frames | 3 | 0 | 16-Apr-14 A | 23-Apr-14 A | |
| L05-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 17-Apr-14 A | 25-Apr-14 A | |
| L06-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 17-Apr-14 A | 12-May-14 A | |
| L06-6023 | Inspection of Exterior Framing | 0 | 0 | 17-Apr-14 A | | |
| L09-8219 | HVAC Risers | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L09-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L04-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 18-Apr-14 A | 20-Apr-14 A | |
| L04-6028 | PreRock at Heat Pumps | 2 | 0 | 20-Apr-14 A | 22-Apr-14 A | |
| L08-8219 | HVAC Risers | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6009 | Inspect Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6011 | PreRock Shafts | 2 | 0 | 22-Apr-14 A | 24-Apr-14 A | |
| L04-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L06-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 23-Apr-14 A | 25-Apr-14 A | |
| L08-6020 | Install Hollow Metal Frames | 3 | 0 | 23-Apr-14 A | 13-May-14 A | |
| L11-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L11-8220 | Plumbing Risers - Install | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |

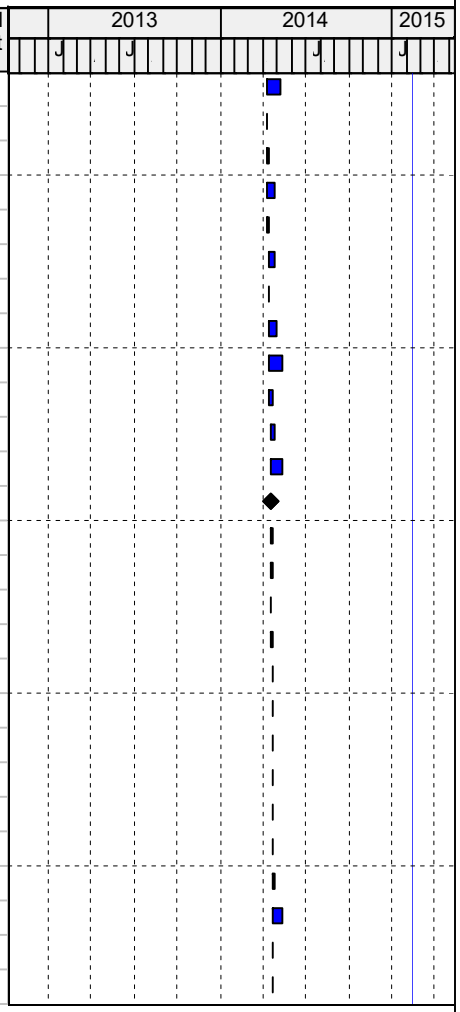


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L09-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L10-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L10-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 20-May-14 A | |
| L12-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L04-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 25-Apr-14 A | 11-Jun-14 A | |
| L04-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L09-6010 | Frame Walls | 5 | 0 | 25-Apr-14 A | 20-May-14 A | |
| L09-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L10-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L11-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 30-Apr-14 A | |
| L12-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L08-6010 | Frame Walls | 5 | 0 | 26-Apr-14 A | 30-Apr-14 A | |
| L10-6002 | Layout | 5 | 0 | 27-Apr-14 A | 27-Apr-14 A | |
| L04-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 28-Apr-14 A | 30-Apr-14 A | |
| L05-6018 | HVAC RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6028 | PreRock at Heat Pumps | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L07-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 28-Apr-14 A | 12-May-14 A | |
| L10-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-Apr-14 A | 22-May-14 A | |
| L11-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L12-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L05-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| L05-6028 | PreRock at Heat Pumps | 2 | 0 | 29-Apr-14 A | 29-Apr-14 A | |

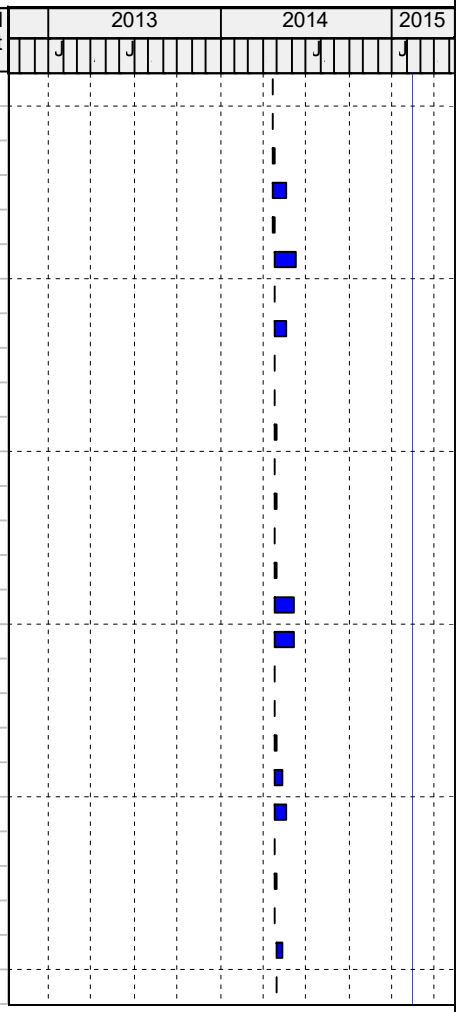



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L06-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 09-May-14 A | |
| L06-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L06-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L08-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L08-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L09-6020 | Install Hollow Metal Frames | 3 | 0 | 29-Apr-14 A | 20-May-14 A | |
| L09-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L10-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L04-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 30-Apr-14 A | 02-May-14 A | |
| L09-6019 | Complete Top Out GWB | 2 | 0 | 30-Apr-14 A | 06-Jun-14 A | |
| L11-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L12-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L03-6028 | PreRock at Heat Pumps | 2 | 0 | 01-May-14 A | 02-May-14 A | |
| L05-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L06-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L03-6014 | Set Tubs & Plumbing RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L05-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L05-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| L06-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L06-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 09-May-14 A | |
| L03-6018 | HVAC RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |

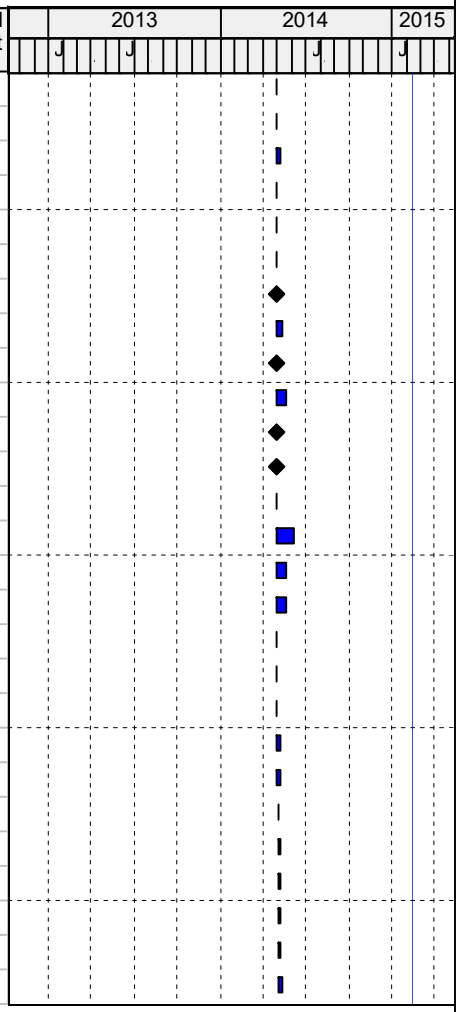


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 06-May-14 A | 06-May-14 A | |
| L07-6014 | Set Tubs & Plumbing RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L07-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 06-May-14 A | 09-May-14 A | |
| L03-6004 | CMU Wall/Clips | 3 | 0 | 07-May-14 A | 08-May-14 A | |
| L03-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L03-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 08-May-14 A | 13-May-14 A | |
| L03-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6004 | CMU Walls | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6018 | HVAC RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L11-6010 | Frame Walls | 5 | 0 | 09-May-14 A | 15-May-14 A | |
| L05-6014 | Set Tubs & Plumbing RI | 5 | 0 | 12-May-14 A | 05-Jun-14 A | |
| L07-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 12-May-14 A | 13-May-14 A | |
| L11-6020 | Install Hollow Metal Frames | 3 | 0 | 12-May-14 A | 14-May-14 A | |
| L11-6019 | Complete Top Out GWB | 2 | 0 | 12-May-14 A | 14-May-14 A | |
| L14-6002 | Layout | 5 | 0 | 12-May-14 A | 14-May-14 A | |
| L15-6002 | Layout | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L05-6004 | CMU Walls | 3 | 0 | 13-May-14 A | 13-May-14 A | |
| L06-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 25-Jun-14 A | |
| L06-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 13-May-14 A | 14-Jul-14 A | |
| L07-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 05-Jun-14 A | |
| L07-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| L07-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 13-May-14 A | 13-May-14 A | |
| L14-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L16-6002 | Layout | 5 | 0 | 13-May-14 A | 16-May-14 A | |

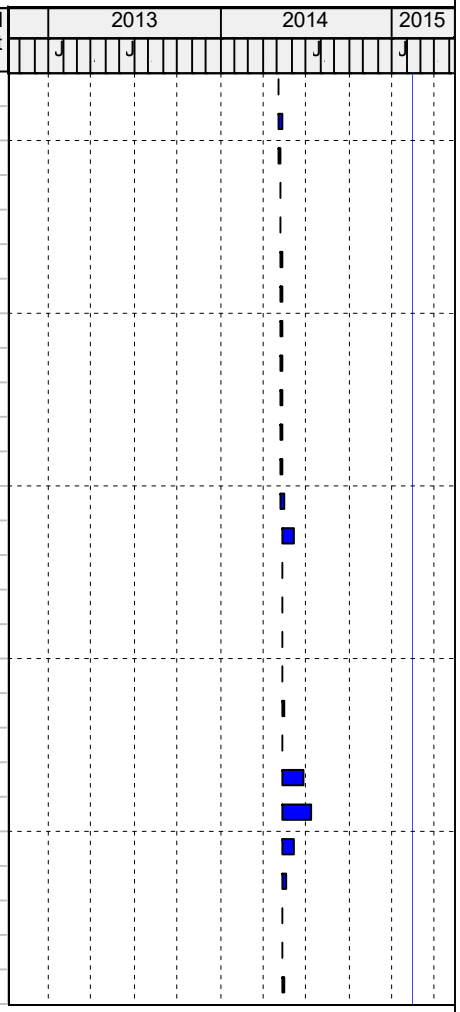



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-6004 | CMU Walls | 3 | 0 | 14-May-14 A | 14-May-14 A | |
| L07-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 15-May-14 A | |
| L08-6012 | Fire Sprinkler Mains | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6002 | Layout | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L07-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6014 | Set Tubs & Plumbing RI | 5 | 0 | 16-May-14 A | 25-Jun-14 A | |
| L08-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L11-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L12-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L07-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L08-6028 | PreRock at Heat Pumps | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L09-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L10-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L11-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L15-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 19-May-14 A | 19-May-14 A | |
| L07-6028 | PreRock at Heat Pumps | 2 | 0 | 20-May-14 A | 21-May-14 A | |
| L07-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L08-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 20-May-14 A | 21-May-14 A | |
| L10-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L11-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L14-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |

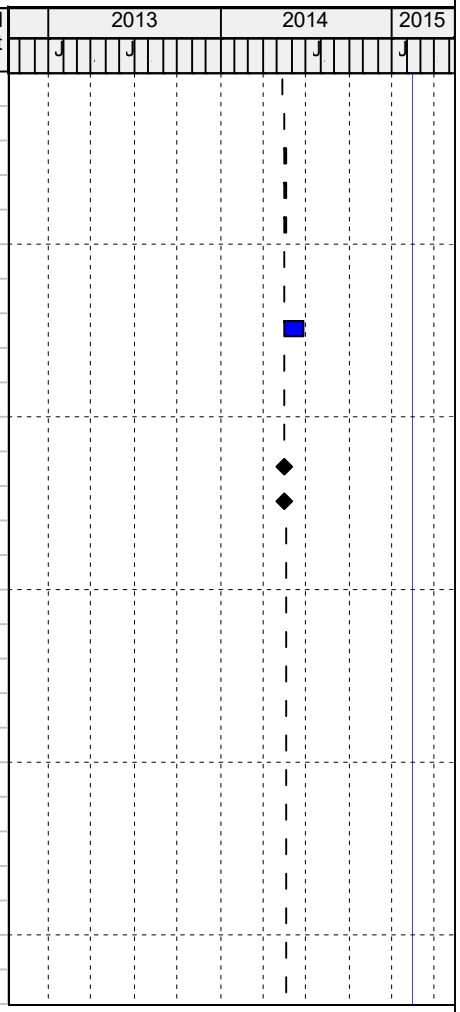



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 21-May-14 A | 27-May-14 A | |
| L08-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L08-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L09-6028 | PreRock at Heat Pumps | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L10-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 21-May-14 A | 27-Jun-14 A | |
| L10-6010 | Frame Walls | 5 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6019 | Complete Top Out GWB | 2 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L11-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L12-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L14-8220 | Plumbing Risers - Install | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L15-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L16-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L07-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| L08-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 22-May-14 A | 22-May-14 A | |
| L10-6012 | Fire Sprinkler Mains | 5 | 0 | 22-May-14 A | 27-May-14 A | |
| L08-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L09-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6020 | Install Hollow Metal Frames | 3 | 0 | 23-May-14 A | 03-Jun-14 A | |
| L10-6028 | PreRock at Heat Pumps | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L14-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L15-8220 | Plumbing Risers - Install | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L09-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 27-May-14 A | 27-May-14 A | |
| L12-6010 | Frame Walls | 5 | 0 | 27-May-14 A | 02-Jun-14 A | |
| L08-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L09-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 28-May-14 A | 28-May-14 A | |
| L10-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 28-May-14 A | 03-Jun-14 A | |

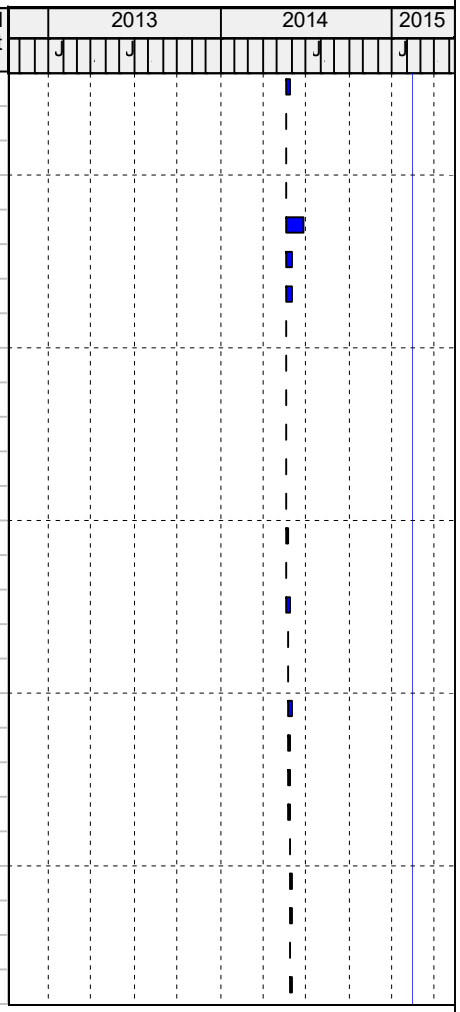



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L15-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-May-14 A | 30-May-14 A | |
| L16-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 28-May-14 A | 28-May-14 A | |
| L16-8220 | Plumbing Risers - Install | 2 | 0 | 28-May-14 A | 29-May-14 A | |
| L08-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 29-May-14 A | 30-May-14 A | |
| L10-6016 | Electrical RI | 5 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L10-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| L12-6012 | Fire Sprinkler Mains | 5 | 0 | 30-May-14 A | 26-Jun-14 A | |
| L12-6020 | Install Hollow Metal Frames | 3 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L15-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L17-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L17-8220 | Plumbing Risers - Install | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L10-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L11-6016 | Electrical RI | 5 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L11-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L12-6019 | Complete Top Out GWB | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L14-6020 | Install Hollow Metal Frames | 3 | 0 | 02-Jun-14 A | 05-Jun-14 A | |
| L14-6010 | Frame Walls | 5 | 0 | 02-Jun-14 A | 04-Jun-14 A | |
| L16-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| L14-6019 | Complete Top Out GWB | 2 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L16-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L10-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| L17-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 04-Jun-14 A | 11-Jun-14 A | |
| L08-6016 | Electrical RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L08-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |

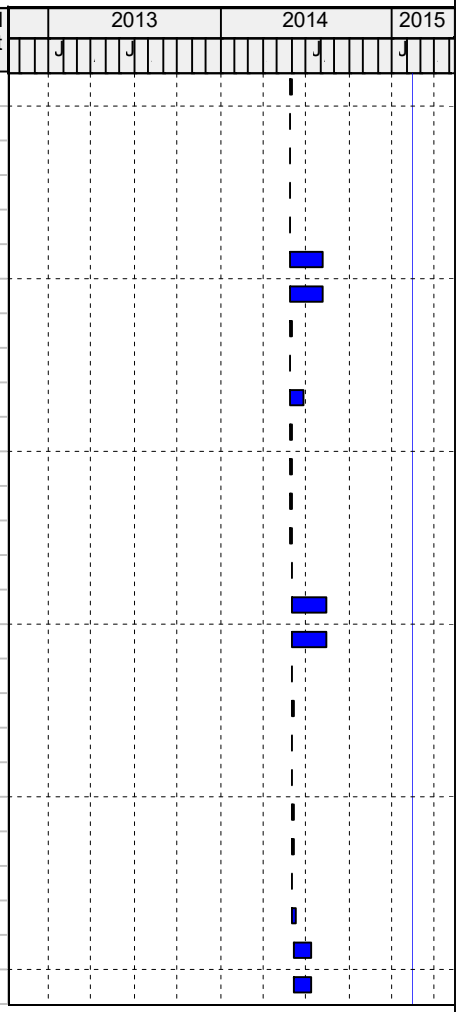



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L12-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L15-6010 | Frame Walls | 3 | 0 | 05-Jun-14 A | 11-Jun-14 A | |
| L09-6012 | Fire Sprinkler Mains | 5 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L09-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L11-6012 | Fire Sprinkler Mains | 4 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L12-6014 | Set Tubs & Plumbing RI | 4 | 0 | 06-Jun-14 A | 27-Jun-14 A | |
| L11-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jun-14 A | 11-Jun-14 A | |
| L09-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-Jun-14 A | 25-Jun-14 A | |
| L14-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L15-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L16-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L09-6016 | Electrical RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L14-6014 | Set Tubs & Plumbing RI | 4 | 0 | 10-Jun-14 A | 21-Jul-14 A | |
| L15-6020 | Install Hollow Metal Frames | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L15-6019 | Complete Top Out GWB | 2 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6014 | Set Tubs & Plumbing RI | 4 | 0 | 11-Jun-14 A | 26-Jun-14 A | |
| L11-6028 | PreRock at Heat Pumps | 2 | 0 | 13-Jun-14 A | 14-Jun-14 A | |
| L11-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 14-Jun-14 A | 14-Jun-14 A | |
| L14-6012 | Fire Sprinkler Mains | 2 | 0 | 16-Jun-14 A | 27-Jun-14 A | |
| L14-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 18-Jun-14 A | 18-Jun-14 A | |
| L15-6023 | Inspection of Exterior Framing | 0 | 0 | 18-Jun-14 A | | |
| L17-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 18-Jun-14 A | 23-Jun-14 A | |
| L17-6010 | Frame Walls | 5 | 0 | 18-Jun-14 A | 29-Jul-14 A | |

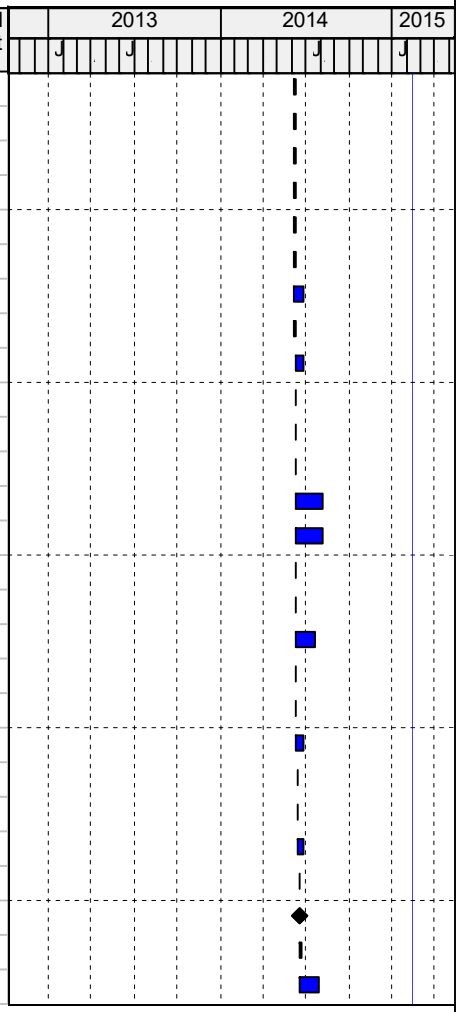


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L12-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6023 | Inspection of Exterior Framing | 0 | 0 | 20-Jun-14 A | | |
| L15-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-Jun-14 A | 20-Jun-14 A | |
| L10-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-Jun-14 A | 23-Jun-14 A | |
| L15-6014 | Set Tubs & Plumbing RI | 5 | 0 | 22-Jun-14 A | 24-Jul-14 A | |
| L08-6018 | HVAC RI | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L12-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L14-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L15-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L08-6221 | Frame Unit Ceilings | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| L11-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 24-Jun-14 A | 27-Jun-14 A | |
| L12-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L14-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6023 | Inspection of Exterior Framing | 0 | 0 | 24-Jun-14 A | | |
| L12-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| L12-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L14-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L15-6012 | Fire Sprinkler Mains | 2 | 0 | 25-Jun-14 A | 22-Jul-14 A | |
| L16-6023 | Inspection of Exterior Framing | 0 | 0 | 25-Jun-14 A | | |
| L03-6024 | Inspections for GWB Cover | 1 | 0 | 27-Jun-14 A | 27-Jun-14 A | |
| L09-6018 | HVAC RI | 3 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L09-6221 | Frame Unit Ceilings | 2 | 0 | 27-Jun-14 A | 30-Jun-14 A | |
| L12-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |

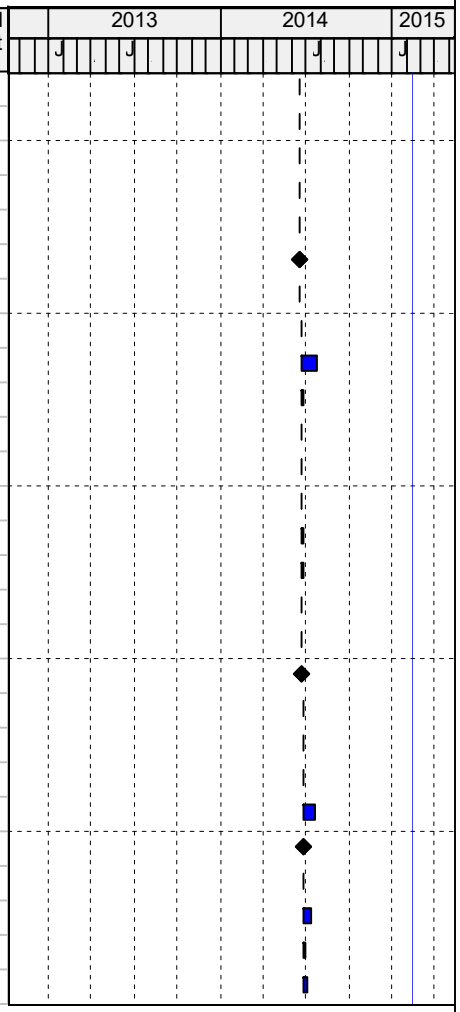


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L15-6028 | PreRock at Heat Pumps | 2 | 0 | 30-Jun-14 A | 01-Jul-14 A | |
| L16-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 0 | 30-Jun-14 A | 30-Jun-14 A | |
| L16-6010 | Frame Walls | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| L16-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L15-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L15-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L04-6024 | Inspections for GWB Cover | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L10-6018 | HVAC RI | 3 | 0 | 07-Jul-14 A | 21-Jul-14 A | |
| L11-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L15-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L16-6012 | Fire Sprinkler Mains | 2 | 0 | 07-Jul-14 A | 24-Jul-14 A | |
| L16-6020 | Install Hollow Metal Frames | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L16-6028 | PreRock at Heat Pumps | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L17-6019 | Complete Top Out GWB | 1 | 0 | 07-Jul-14 A | 08-Aug-14 A | |
| L11-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L15-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 08-Jul-14 A | 04-Aug-14 A | |
| L17-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jul-14 A | 01-Aug-14 A | |
| L10-6221 | Frame Unit Ceilings | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| L17-6012 | Fire Sprinkler Mains | 2 | 0 | 09-Jul-14 A | 12-Aug-14 A | |
| L05-6024 | Inspections for GWB Cover | 2 | 0 | 10-Jul-14 A | 10-Jul-14 A | |
| L04-6000 | Tape/Finish GWB | 6 | 0 | 11-Jul-14 A | 23-Jul-14 A | |
| L16-6019 | Complete Top Out GWB | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L16-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L15-6018 | HVAC RI | 3 | 0 | 16-Jul-14 A | 18-Jul-14 A | |
| L16-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-6024 | Inspections for GWB Cover | 2 | 0 | 17-Jul-14 A | 17-Jul-14 A | |

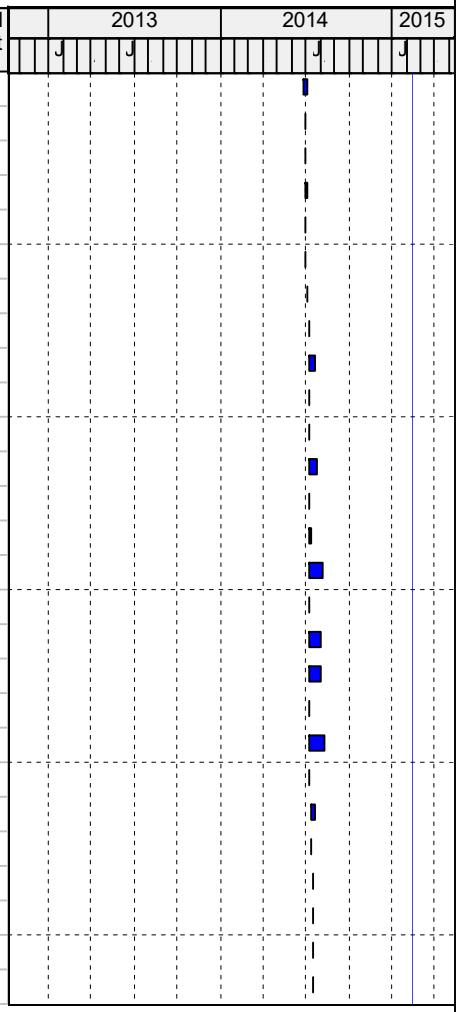



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6018 | HVAC RI | 3 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L16-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 21-Jul-14 A | 18-Aug-14 A | |
| L15-6013 | Fire Sprinkler Branch Lines | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| L03-6000 | Tape/Finish GWB | 6 | 0 | 23-Jul-14 A | 29-Jul-14 A | |
| L11-6018 | HVAC RI | 3 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L15-6221 | Frame Unit Ceilings | 2 | 0 | 23-Jul-14 A | 01-Aug-14 A | |
| L16-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L17-6020 | Install Hollow Metal Frames | 3 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| L11-6221 | Frame Unit Ceilings | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L12-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L14-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L14-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L16-6014 | Set Tubs & Plumbing RI | 5 | 0 | 28-Jul-14 A | 18-Aug-14 A | |
| L07-6024 | Inspections for GWB Cover | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L12-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L05-6000 | Tape/Finish GWB | 6 | 0 | 31-Jul-14 A | 05-Aug-14 A | |
| L08-6024 | Inspections for GWB Cover | 2 | 0 | 31-Jul-14 A | 31-Jul-14 A | |
| L12-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L14-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L06-6000 | Tape/Finish GWB | 4 | 0 | 06-Aug-14 A | 11-Aug-14 A | |
| L09-6024 | Inspections for GWB Cover | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |

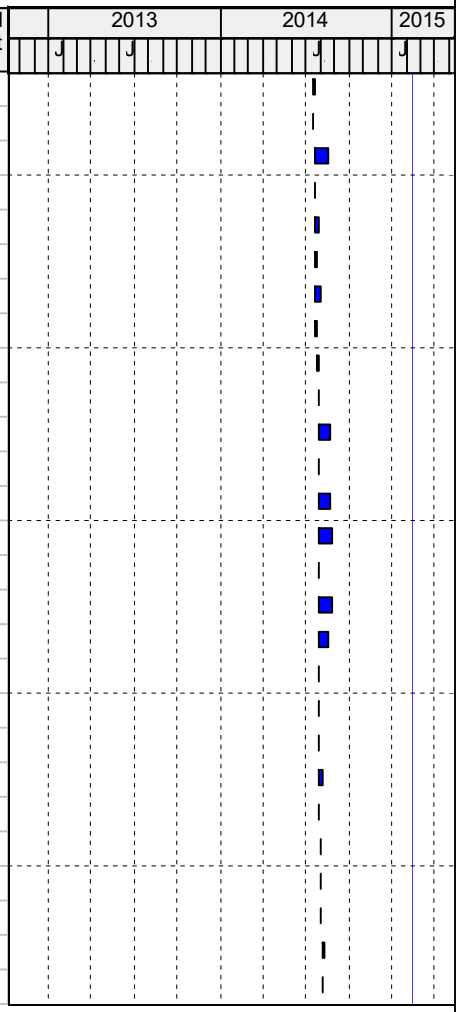



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6000 | Tape/Finish GWB | 5 | 0 | 07-Aug-14 A | 16-Aug-14 A | |
| L11-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 08-Aug-14 A | 14-Aug-14 A | |
| L17-6014 | Set Tubs & Plumbing RI | 5 | 0 | 08-Aug-14 A | 16-Sep-14 A | |
| L10-6024 | Inspections for GWB Cover | 2 | 0 | 11-Aug-14 A | 12-Aug-14 A | |
| L09-6000 | Tape/Finish GWB | 5 | 0 | 14-Aug-14 A | 19-Aug-14 A | |
| L08-6000 | Tape/Finish GWB | 5 | 0 | 16-Aug-14 A | 21-Aug-14 A | |
| L11-6024 | Inspections for GWB Cover | 2 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L16-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 18-Aug-14 A | 29-Aug-14 A | |
| L10-6000 | Tape/Finish GWB | 5 | 0 | 19-Aug-14 A | 23-Aug-14 A | |
| L16-6221 | Frame Unit Ceilings | 4 | 0 | 21-Aug-14 A | 26-Aug-14 A | |
| L17-6018 | HVAC RI | 3 | 0 | 21-Aug-14 A | 10-Sep-14 A | |
| L12-6024 | Inspections for GWB Cover | 2 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L15-6016 | Electrical RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L15-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L11-6000 | Tape/Finish GWB | 5 | 0 | 23-Aug-14 A | 29-Aug-14 A | |
| L17-6221 | Frame Unit Ceilings | 4 | 0 | 26-Aug-14 A | 28-Aug-14 A | |
| L14-6024 | Inspections for GWB Cover | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L16-6016 | Electrical RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L16-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L12-6000 | Tape/Finish GWB | 5 | 0 | 02-Sep-14 A | 08-Sep-14 A | |
| L15-6024 | Inspections for GWB Cover | 2 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L14-6000 | Tape/Finish GWB | 5 | 0 | 06-Sep-14 A | 11-Sep-14 A | |
| L15-6000 | Tape/Finish GWB | 4 | 0 | 12-Sep-14 A | 20-Sep-14 A | |
| L17-6016 | Electrical RI | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |

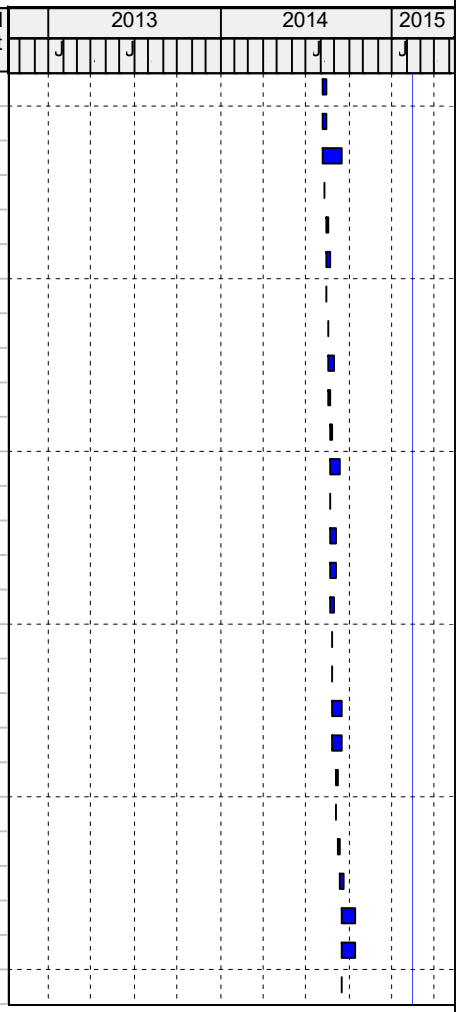



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6028 | PreRock at Heat Pumps | 2 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L17-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L17-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L17-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 24-Sep-14 A | 27-Sep-14 A | |
| L17-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L16-6024 | Inspections for GWB Cover | 1 | 0 | 08-Oct-14 A | 09-Oct-14 A | |
| L16-6000 | Tape/Finish GWB | 4 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6024 | Inspections for GWB Cover | 1 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6000 | Tape/Finish GWB | 6 | 0 | 30-Oct-14 A | 07-Nov-14 A | |
| **Mechanical Penthouse** | | | | | | |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 0 | 11-Jun-14 A | 20-Jun-14 A | |
| PH-6006 | PH - Exterior Wall Framing (including PH roof parapet | 6 | 0 | 12-Jun-14 A | 14-Jul-14 A | |
| PH-6014 | PH - Plumbing/Piping Rl | 40 | 0 | 25-Jun-14 A | 05-Nov-14 A | |
| PH-6002 | PH - Layout | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| PH-6008 | PH - Interior Wall Framing | 3 | 0 | 24-Jul-14 A | 08-Aug-14 A | |
| PH-6020 | PH - H Mtl Frames | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| PH-6012 | PH - Fire Sprinkler Rl | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |
| PH-6018 | PH - HVAC Rl | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |
| PH-6016 | PH - Electrical Rl | 10 | 0 | 23-Sep-14 A | 14-Nov-14 A | |
| PH-6022 | PH - Fire Alarm / Elec Specialties Rl | 10 | 0 | 23-Sep-14 A | 14-Nov-14 A | |
| **Finishes** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL4-8100 | LL4 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |

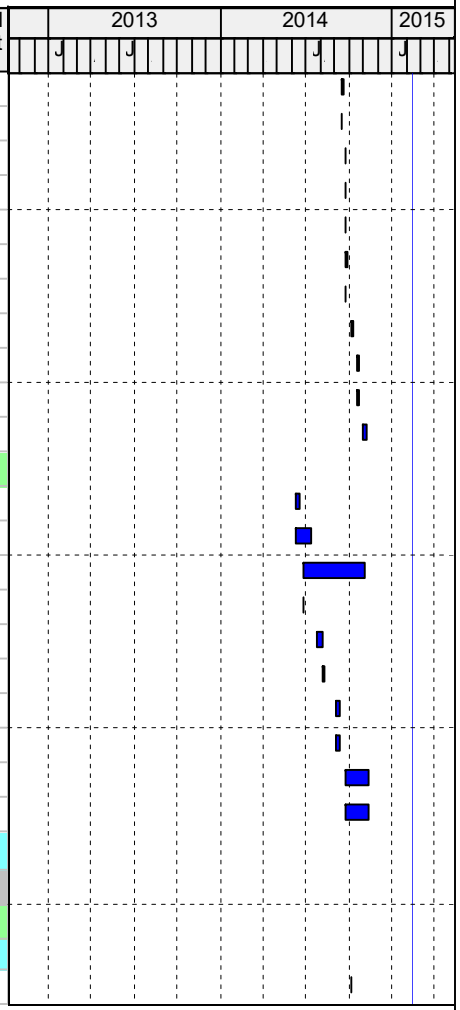


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8102 | LL4 - GWB Hang (incl. screw inspection) | 3 | 0 | 27-Oct-14 A | 10-Dec-14 A | |
| LL4-8114 | LL4 - Striping / Signage (DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL4-8104 | LL4 - Int Painting | 3 | 0 | 22-Dec-14 A | 24-Dec-14 A | |
| LL4-8122 | LL4 - Plumbing Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL4-8108 | Electrical trim & finish | 5 | 1 | 29-Dec-14 A | 16-Feb-15 | 22 |
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL4-8126 | Install doors & hardware | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL4-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 22-Jan-15 A | 26-Jan-15 A | |
| LL4-8124 | Flooring - VCT | 4 | 0 | 05-Feb-15 A | 06-Feb-15 A | |
| LL4-8110 | HVAC trim | 2 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| LL4-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 12-Mar-15 | 18-Mar-15 | 22 |
| LL4-8134 | Final Cleaning | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 22 |
| LL4-8214 | Floor Complete | 0 | 0 | | 19-Mar-15 | 22 |
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL3-8100 | LL3 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| LL3-8102 | LL3 - GWB Hang (incl. screw inspection) | 3 | 0 | 27-Oct-14 A | 10-Dec-14 A | |
| LL3-8114 | LL3 - Striping / Signage [DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL3-8104 | LL3 - Int Painting | 3 | 0 | 22-Dec-14 A | 24-Dec-14 A | |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL3-8108 | Electrical trim & finish | 5 | 1 | 29-Dec-14 A | 16-Feb-15 | 22 |
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL3-8126 | Install doors & hardware | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL3-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 22-Jan-15 A | 03-Feb-15 A | |
| LL3-8124 | Flooring - VCT | 4 | 0 | 06-Feb-15 A | 07-Feb-15 A | |
| LL3-8110 | HVAC trim | 2 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| LL3-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 12-Mar-15 | 18-Mar-15 | 22 |

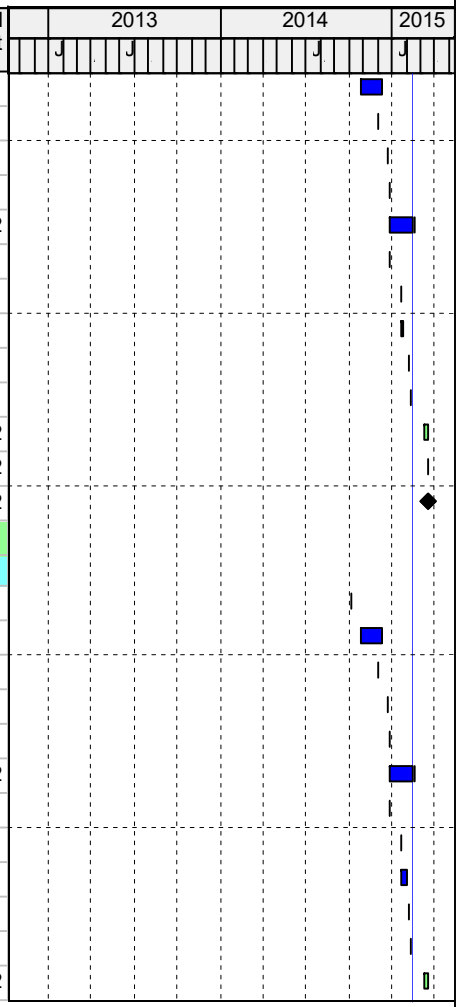



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-8134 | Final Cleaning | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 22 |
| LL3-8214 | Floor Complete | 0 | 0 | | 19-Mar-15 | 22 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL2E-8102 | LL2 - GWB Hang / Tape / Finish @ Electrical Rooms | 8 | 0 | 24-Jun-14 A | 03-Jul-14 A | |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish & Inspection | 6 | 0 | 16-Sep-14 A | 22-Dec-14 A | |
| LL2-8100 | LL2 - Insulation | 5 | 0 | 16-Sep-14 A | 09-Oct-14 A | |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 5 | 0 | 17-Sep-14 A | 27-Oct-14 A | |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| LL2-8104 | LL2 - Int Painting | 5 | 0 | 25-Nov-14 A | 23-Dec-14 A | |
| LL2-8114 | LL2 - Striping / Signage [DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL2-8116 | LL2 - Finish Carpentry / Millwork [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL2-8124 | Flooring - VCT | 4 | 0 | 06-Feb-15 A | 07-Feb-15 A | |
| LL2-8126 | Install doors & hardware | 3 | 1 | 09-Feb-15 A | 16-Feb-15 | 32 |
| LL2-8122 | Complete MEP trim | 3 | 3 | 25-Mar-15 | 27-Mar-15 | 3 |
| LL2-8128 | Entry Gates at Garage | 5 | 5 | 30-Mar-15 | 03-Apr-15 | 11 |
| LL2-8136 | Chainlink Fencing / Gate @ Recycling at Garage | 5 | 5 | 30-Mar-15 | 03-Apr-15 | 11 |
| LL2-8120 | Install bollards at Garage | 5 | 5 | 30-Mar-15 | 03-Apr-15 | 11 |
| LL2-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 08-Apr-15 | 14-Apr-15 | 3 |
| LL2-8134 | Final Cleaning | 2 | 2 | 14-Apr-15 | 15-Apr-15 | 3 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 31-Jul-14 A | |
| LL1-Z2U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 09-May-14 A | |
| LL1-Z3U-8102 | Above Ceiling GWB (At All Areas North of Q-Line) | 5 | 0 | 10-Feb-14 A | 20-Jun-14 A | |
| L1BU-8102 | Above Ceiling GWB [including East Service Corridor] | 5 | 0 | 06-Jun-14 A | 11-Jun-14 A | |
| L1LU-8102 | Above Ceiling GWB | 5 | 0 | 24-Jun-14 A | 13-Oct-14 A | |

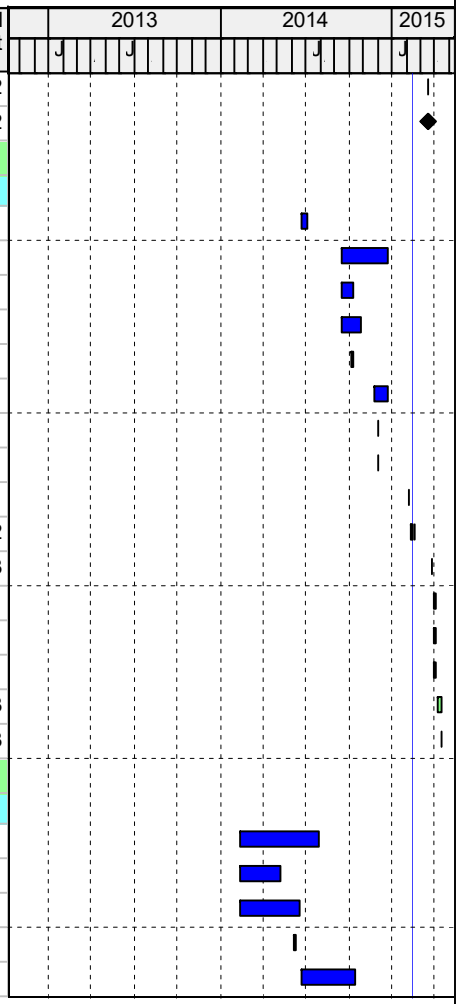



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1KU-8102 | Above Ceiling GWB | 2 | 0 | 26-Jun-14 A | 22-Aug-14 A | |
| LL1-8100 | Insulation | 5 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| LL1-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 28-Jul-14 A | 06-Aug-14 A | |
| LL1-Z2-8102 | GWB Hang (Walls) & Inspection | 4 | 0 | 11-Aug-14 A | 14-Aug-14 A | |
| LL1-Z2-8100 | Insulation | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| LL1-8215 | GWB Tape (Walls) | 10 | 0 | 16-Aug-14 A | 07-Nov-14 A | |
| LL1-Z3-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 15-Sep-14 A | 07-Oct-14 A | |
| LL1-Z3-8100 | Insulation | 5 | 0 | 15-Sep-14 A | 24-Sep-14 A | |
| LL1-Z2-8215 | GWB Tape (Walls/Ceilings) | 7 | 0 | 29-Sep-14 A | 07-Nov-14 A | |
| L1B-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L1K-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| LL1-Z3-8215 | GWB Tape (Walls & Ceilings) | 7 | 0 | 07-Oct-14 A | 18-Nov-14 A | |
| L1K-8102 | GWB Hang (Walls) & Inspection | 8 | 0 | 09-Oct-14 A | 31-Oct-14 A | |
| L1L-8100 | Insulation | 4 | 0 | 13-Oct-14 A | 16-Oct-14 A | |
| L1B-8102 | GWB Hang (Walls) & Inspection - Main Ballroom N/S/ | 4 | 0 | 16-Oct-14 A | 22-Oct-14 A | |
| L1L-8102 | GWB hang walls (Dining & Lounge) | 4 | 0 | 30-Oct-14 A | 05-Feb-15 A | |
| L1K-8215 | GWB Tape (Walls & Ceilings) | 4 | 0 | 05-Nov-14 A | 18-Nov-14 A | |
| LL1-Z3-8104 | Prime Paint | 4 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| LL1-8104 | Prime Paint & First Coat Finish Paint | 5 | 0 | 02-Dec-14 A | 12-Dec-14 A | |
| L1K-8106 | Wall coverings - FRP | 8 | 0 | 19-Dec-14 A | 08-Jan-15 A | |
| LL1-Z3-8114 | Ceiling grid & inspection | 4 | 0 | 13-Jan-15 A | 16-Jan-15 A | |
| LL1-8126 | Install doors & hardware | 5 | 0 | 26-Jan-15 A | 03-Feb-15 A | |
| L1L-8215 | GWB hang ceilings (Dining & Lounge) | 5 | 0 | 29-Jan-15 A | 05-Feb-15 A | |
| LL1-8116 | Finish carpentry/millwork | 10 | 5 | 05-Feb-15 A | 20-Feb-15 | 18 |
| L1K-8114 | Ceiling grid & inspection | 8 | 4 | 05-Feb-15 A | 19-Feb-15 | 5 |
| LL1-Z3-8126 | Install doors & hardware | 5 | 0 | 09-Feb-15 A | 12-Feb-15 A | |
| L1K-8124 | Flooring - VCT | 3 | 2 | 10-Feb-15 A | 24-Feb-15 | 25 |

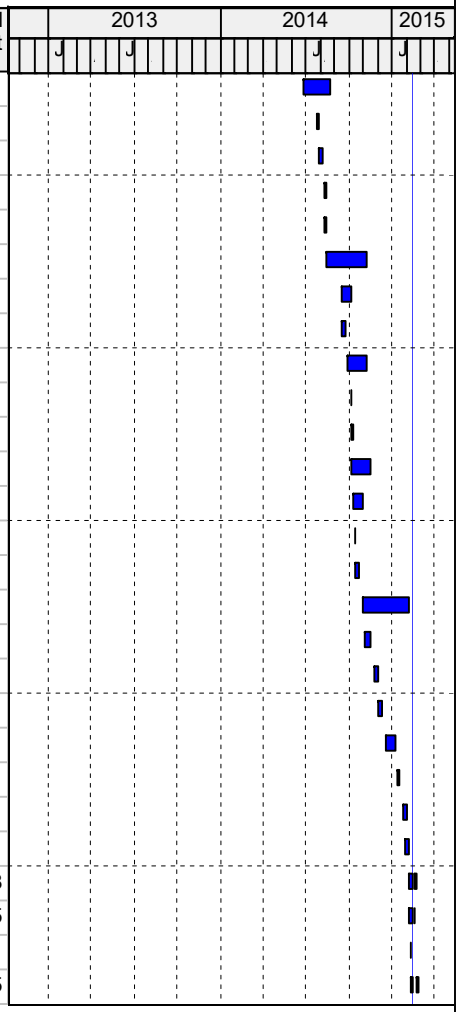


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-8114 | Ceiling grid & inspection | 4 | 2 | 11-Feb-15 A | 17-Feb-15 | 17 |
| LL1-8118 | Lighting & electrical drops to grid | 3 | 2 | 12-Feb-15 A | 19-Feb-15 | 17 |
| L1L-8104 | Paint, prime | 2 | 1 | 13-Feb-15 A | 17-Feb-15 | 3 |
| LL1-8124 | Flooring - VCT at storage areas, janitorial, mechanica | 5 | 5 | 16-Feb-15 | 20-Feb-15 | 28 |
| LL1-Z2-8114 | Ceiling grid & inspection | 5 | 5 | 16-Feb-15 | 20-Feb-15 | 16 |
| LL1-Z2-8104 | Paint, prime at Jr. Ballrooms | 2 | 2 | 18-Feb-15 | 19-Feb-15 | 14 |
| L1L-8114 | Install 9-wood ceiling supports - north of Grid K | 3 | 3 | 18-Feb-15 | 20-Feb-15 | 5 |
| LL1-8112 | Fire sprinkler drops to grid | 2 | 2 | 20-Feb-15 | 23-Feb-15 | 17 |
| LL1-Z2-8116 | Finish carpentry/millwork | 10 | 10 | 20-Feb-15 | 05-Mar-15 | 14 |
| L1L-8106 | Wall coverings - vinyl | 5 | 5 | 20-Feb-15 | 26-Feb-15 | 3 |
| L1K-8104 | Paint, prime | 2 | 2 | 20-Feb-15 | 23-Feb-15 | 1 |
| LL1-Z2-8106 | Wall coverings - vinyl at Jr. Ballrooms | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 14 |
| LL1-Z3-8124 | Flooring - epoxy at Food Prep | 7 | 7 | 23-Feb-15 | 03-Mar-15 | 9 |
| LL1-Z2-8126 | Install doors & hardware | 3 | 3 | 25-Feb-15 | 27-Feb-15 | 15 |
| LL1-Z2-8118 | Lighting & electrical drops to grid | 3 | 3 | 25-Feb-15 | 27-Feb-15 | 19 |
| L1L-8126 | Install doors & hardware | 4 | 4 | 26-Feb-15 | 03-Mar-15 | 9 |
| L1L-8140 | Install 9-wood ceiling - north of Grid K | 5 | 5 | 27-Feb-15 | 05-Mar-15 | 3 |
| L1K-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 27-Feb-15 | 02-Mar-15 | 1 |
| LL1-Z2-8112 | Fire sprinkler drops to grid | 2 | 2 | 02-Mar-15 | 03-Mar-15 | 20 |
| L1K-8112 | Fire sprinkler trim | 1 | 1 | 03-Mar-15 | 03-Mar-15 | 2 |
| LL1-Z2-8124 | Flooring - VCT at service corridor | 2 | 2 | 04-Mar-15 | 05-Mar-15 | 20 |
| L1B-8114 | Ceiling grid & inspection | 4 | 4 | 05-Mar-15 | 10-Mar-15 | 3 |
| LL1-8140 | Acoustical ceiling tile | 3 | 3 | 10-Mar-15 | 12-Mar-15 | 17 |
| LL1-Z3-8118 | Lighting & electrical drops at ceiling | 3 | 3 | 10-Mar-15 | 12-Mar-15 | 12 |
| L1L-8112 | Fire sprinkler trim - north of Grid K | 1 | 1 | 11-Mar-15 | 11-Mar-15 | 11 |
| L1L-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 1 | 11-Mar-15 | 11-Mar-15 | 11 |
| L1B-8104 | Paint, prime & first coat finish at West Ballrooms | 3 | 3 | 12-Mar-15 | 16-Mar-15 | 2 |

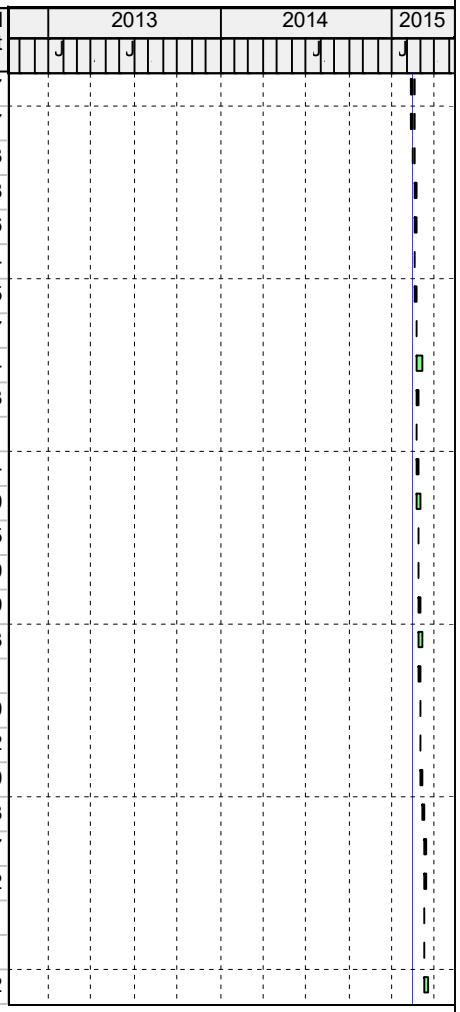



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8112 | Fire sprinkler drops/trim at ceiling | 2 | 2 | 13-Mar-15 | 16-Mar-15 | 12 |
| L1L-8124 | Flooring - wood - north of Grid K | 5 | 5 | 13-Mar-15 | 19-Mar-15 | 10 |
| LL1-Z2-8140 | Acoustical ceiling tile | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 14 |
| LL1-Z3-8116 | Finish carpentry/millwork | 3 | 3 | 17-Mar-15 | 19-Mar-15 | 9 |
| LL1-Z3-8140 | Acoustical ceiling tile | 3 | 3 | 20-Mar-15 | 24-Mar-15 | 9 |
| L1L-8116 | Finish carpentry/millwork - north of Grid K | 10 | 10 | 20-Mar-15 | 02-Apr-15 | 10 |
| LL1-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 4 | 4 | 23-Mar-15 | 26-Mar-15 | 16 |
| L1B-8126 | Install doors & hardware at Ballrooms | 5 | 5 | 23-Mar-15 | 27-Mar-15 | 4 |
| LL1-Z2-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 4 | 4 | 25-Mar-15 | 30-Mar-15 | 14 |
| LL1-8134 | Final Cleaning | 2 | 2 | 26-Mar-15 | 27-Mar-15 | 16 |
| L1K-8116 | Finish carpentry/millwork | 2 | 2 | 26-Mar-15 | 27-Mar-15 | 4 |
| L1K-8126 | Install doors & hardware | 3 | 3 | 26-Mar-15 | 30-Mar-15 | 1 |
| L1K-8140 | Acoustical ceiling tile | 2 | 2 | 27-Mar-15 | 30-Mar-15 | 5 |
| LL1-Z2-8134 | Final Cleaning | 2 | 2 | 30-Mar-15 | 31-Mar-15 | 14 |
| LL1-Z3-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 4 | 4 | 01-Apr-15 | 06-Apr-15 | 9 |
| L1B-8116 | Finish carpentry/millwork at Ballrooms | 10 | 10 | 01-Apr-15 | 14-Apr-15 | 2 |
| LL1-Z3-8134 | Final Cleaning | 2 | 2 | 06-Apr-15 | 07-Apr-15 | 9 |
| L1B-8124 | Flooring - carpet at Ballrooms | 5 | 5 | 10-Apr-15 | 16-Apr-15 | 0 |
| L1K-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 4 | 4 | 13-Apr-15 | 16-Apr-15 | 1 |
| L1K-8134 | Final Cleaning | 2 | 2 | 16-Apr-15 | 17-Apr-15 | 1 |
| L1B-8140 | Acoustical ceiling tile | 2 | 2 | 17-Apr-15 | 20-Apr-15 | 0 |
| L1L-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 4 | 4 | 27-Apr-15 | 30-Apr-15 | 1 |
| L1B-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 4 | 4 | 28-Apr-15 | 01-May-15 | 0 |
| L1L-8134 | Final Cleaning | 2 | 2 | 30-Apr-15 | 01-May-15 | 1 |
| L1B-8134 | Final Cleaning | 2 | 2 | 01-May-15 | 04-May-15 | 0 |
| **Corridors / Common / Public Areas** | | | | | | |
| LL1-8200 | Wall coverings - vinyl | 4 | 0 | 17-Dec-14 A | 19-Jan-15 A | |

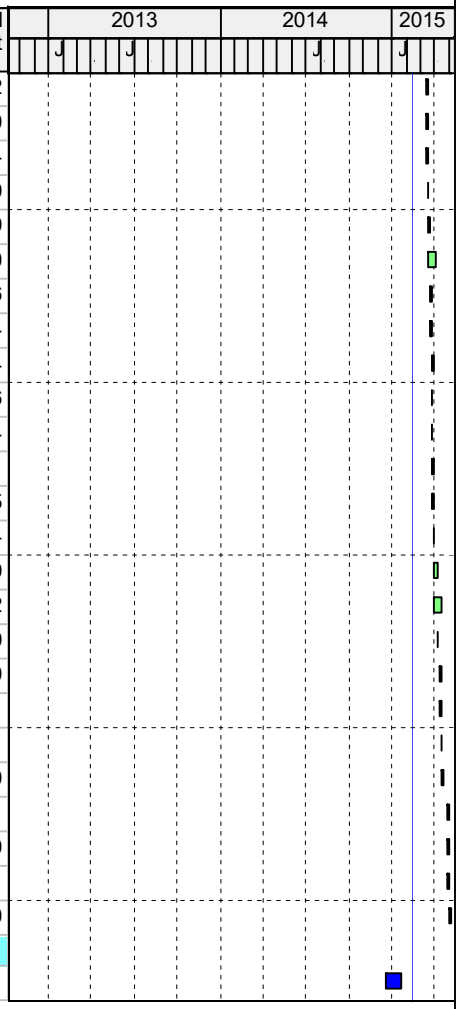


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8200 | Paint, first coat finish | 4 | 0 | 07-Jan-15 A | 12-Jan-15 A | |
| LL1-Z3-8204 | HVAC drops/trim at ceiling | 2 | 1 | 02-Feb-15 A | 16-Feb-15 | 13 |
| LL1-8204 | HVAC drops/trim to grid | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| L1L-8200 | Paint, first coat finish | 2 | 2 | 18-Feb-15 | 19-Feb-15 | 3 |
| LL1-Z2-8200 | Paint, first coat finish at Jr. Ballrooms | 1 | 1 | 20-Feb-15 | 20-Feb-15 | 14 |
| LL1-8201 | Paint, final coat & touch-up | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 29 |
| LL1-Z2-8204 | HVAC drops/trim to grid | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 19 |
| L1K-8200 | Paint, first coat finish | 1 | 1 | 24-Feb-15 | 24-Feb-15 | 1 |
| L1K-8204 | HVAC drops/trim at celing | 2 | 2 | 25-Feb-15 | 26-Feb-15 | 1 |
| L1L-8204 | HVAC trim at ceiling - north of Grid K | 1 | 1 | 06-Mar-15 | 06-Mar-15 | 11 |
| LL1-Z2-8201 | Paint, final coat & touch-up | 2 | 2 | 13-Mar-15 | 16-Mar-15 | 15 |
| L1B-8200 | Paint, prime & first coat finish at East Ballroom | 3 | 3 | 18-Mar-15 | 20-Mar-15 | 0 |
| LL1-Z3-8201 | Paint, final coat & touch-up | 3 | 3 | 20-Mar-15 | 24-Mar-15 | 9 |
| LL1-8214 | LL1, Zone 1 Complete | 0 | 0 | | 27-Mar-15 | 16 |
| LL1-Z2-8214 | LL1 Zone 2 Complete | 0 | 0 | | 31-Mar-15 | 14 |
| L1K-8201 | Paint, final coat & touch-up | 2 | 2 | 02-Apr-15 | 03-Apr-15 | 1 |
| LL1-Z3-8214 | LL1, Zone 3 Complete | 0 | 0 | | 07-Apr-15 | 9 |
| L1L-8201 | Paint, final coat & touch-up | 2 | 2 | 16-Apr-15 | 17-Apr-15 | 1 |
| L1B-8201 | Paint, final coat & touch-up | 2 | 2 | 17-Apr-15 | 20-Apr-15 | 0 |
| L1K-8214 | L1, Zone 1 Complete | 0 | 0 | | 17-Apr-15 | 1 |
| L1L-8214 | L1, Zone 4 Complete | 0 | 0 | | 01-May-15 | 1 |
| L1B-8214 | L1, Zone 2 Complete | 0 | 0 | | 04-May-15 | 0 |
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8100 | L2 - Insulation - North Half | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L02-8102 | L2 - GWB Hang / Tape / Finish - North Half | 7 | 0 | 23-Oct-14 A | 17-Dec-14 A | |
| L02-8104 | Paint, prime & first coat finish at north half | 3 | 3 | 16-Feb-15 | 18-Feb-15 | 3 |

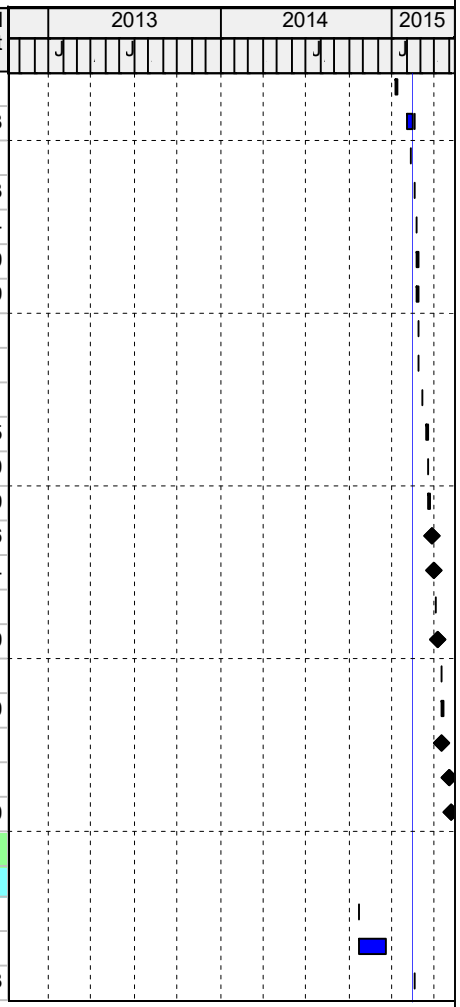


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8106 | Wall coverings - vinyl at south half | 4 | 4 | 16-Feb-15 | 19-Feb-15 | 11 |
| L02-8126 | Install doors & hardware at south half | 5 | 5 | 20-Feb-15 | 26-Feb-15 | 11 |
| L02-8110 | HVAC drops/trim at south half | 2 | 2 | 24-Feb-15 | 25-Feb-15 | 7 |
| L02-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 26-Feb-15 | 02-Mar-15 | 7 |
| L02-8112 | Fire sprinkler drops/trim at south half | 2 | 2 | 03-Mar-15 | 04-Mar-15 | 18 |
| L02-8120 | Ceramic tile | 5 | 5 | 09-Mar-15 | 13-Mar-15 | 3 |
| L02-8124 | Flooring - carpet | 5 | 5 | 09-Mar-15 | 13-Mar-15 | 7 |
| L02-8122 | Plumbing fixtures & trim | 5 | 5 | 16-Mar-15 | 20-Mar-15 | 3 |
| L02-8116 | Finish carpentry/millwork at south half | 4 | 4 | 16-Mar-15 | 19-Mar-15 | 7 |
| L02-8108 | Complete MEP trim at south half | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 7 |
| L02-8128 | Install bathroom accessories | 5 | 5 | 23-Mar-15 | 27-Mar-15 | 3 |
| L02-8136 | Lockers / Benches @ Locker Rooms | 5 | 5 | 23-Mar-15 | 27-Mar-15 | 3 |
| L02-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 08-Apr-15 | 14-Apr-15 | 3 |
| L02-8134 | Final Cleaning | 2 | 2 | 14-Apr-15 | 15-Apr-15 | 3 |
| **Corridors** | | | | | | |
| L02-8200 | Paint, final coat & touch-up at south half | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 7 |
| L02-8214 | Floor Complete | 0 | 0 | | 15-Apr-15 | 3 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L03-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L04-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L05-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L06-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L07-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L08-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L09-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |

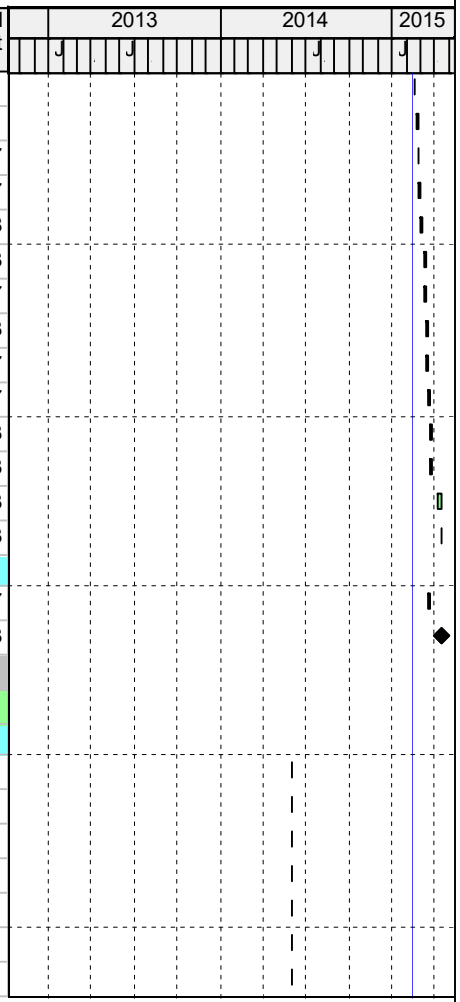



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L11-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L12-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L14-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L15-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L16-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L17-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L03-8102S | Stock GWB | 2 | 0 | 27-Jun-14 A | 08-Jul-14 A | |
| L04-8102 | Hang GWB & Inspection | 4 | 0 | 07-Jul-14 A | 16-Jul-14 A | |
| L04-8102S | Stock GWB | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-8102 | Hang GWB & Inspection | 5 | 0 | 09-Jul-14 A | 22-Jul-14 A | |
| L05-8102S | Stock GWB | 2 | 0 | 10-Jul-14 A | 14-Jul-14 A | |
| L05-8102 | Hang GWB & Inspection | 4 | 0 | 17-Jul-14 A | 23-Jul-14 A | |
| L06-8102S | Stock GWB | 2 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L04-8104 | Paint (Prime) | 2 | 0 | 28-Jul-14 A | 05-Aug-14 A | |
| L03-8104 | Paint (Prime) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L03-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L07-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L08-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L06-8102 | Hang GWB & Inspection | 5 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L07-8102 | Hang GWB & Inspection | 6 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L04-8105 | Paint (First Coat & Ceilings) | 5 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L05-8104 | Paint (Prime) | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| L09-8102S | Stock GWB | 2 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 07-Aug-14 A | 11-Aug-14 A | |
| L09-8102 | Hang GWB & Inspection | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| L08-8102 | Hang GWB & Inspection | 6 | 0 | 11-Aug-14 A | 15-Aug-14 A | |

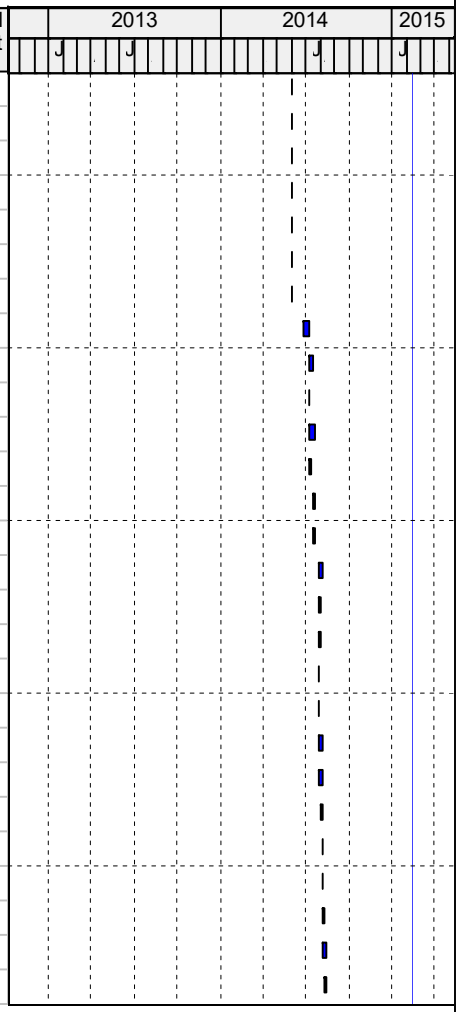



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8104 | Paint (Prime) | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L10-8102S | Stock GWB | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-8102 | Hang GWB & Inspection | 4 | 0 | 13-Aug-14 A | 18-Aug-14 A | |
| L06-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 14-Aug-14 A | 18-Aug-14 A | |
| L11-8102S | Stock GWB | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L07-8104 | Paint (Prime) | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L11-8102 | Hang GWB & Inspection | 4 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| L07-8105 | Paint (First Coat & Ceilings) | 4 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L09-8104 | Paint (Prime) | 2 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L08-8104 | Paint (Prime) | 2 | 0 | 22-Aug-14 A | 25-Aug-14 A | |
| L12-8102 | Hang GWB & Inspection | 4 | 0 | 22-Aug-14 A | 30-Aug-14 A | |
| L12-8102S | Stock GWB | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8108 | Elec Trim / Finish | 4 | 0 | 25-Aug-14 A | 04-Sep-14 A | |
| L08-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L03-8118 | Fire Alarm Trim / Finish | 3 | 0 | 27-Aug-14 A | 29-Sep-14 A | |
| L14-8102S | Stock GWB | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L09-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 29-Aug-14 A | 09-Sep-14 A | |
| L14-8102 | Hang GWB & Inspection | 5 | 0 | 29-Aug-14 A | 05-Sep-14 A | |
| L03-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 02-Sep-14 A | 05-Sep-14 A | |
| L04-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 04-Sep-14 A | 09-Sep-14 A | |
| L10-8104 | Paint (Prime) | 2 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| L15-8102S | Stock GWB | 1 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L15-8102 | Hang GWB & Inspection | 5 | 0 | 06-Sep-14 A | 12-Sep-14 A | |
| L03-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8108 | Elec Trim / Finish | 4 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L04-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 11-Sep-14 A | |
| L05-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 08-Sep-14 A | 12-Sep-14 A | |

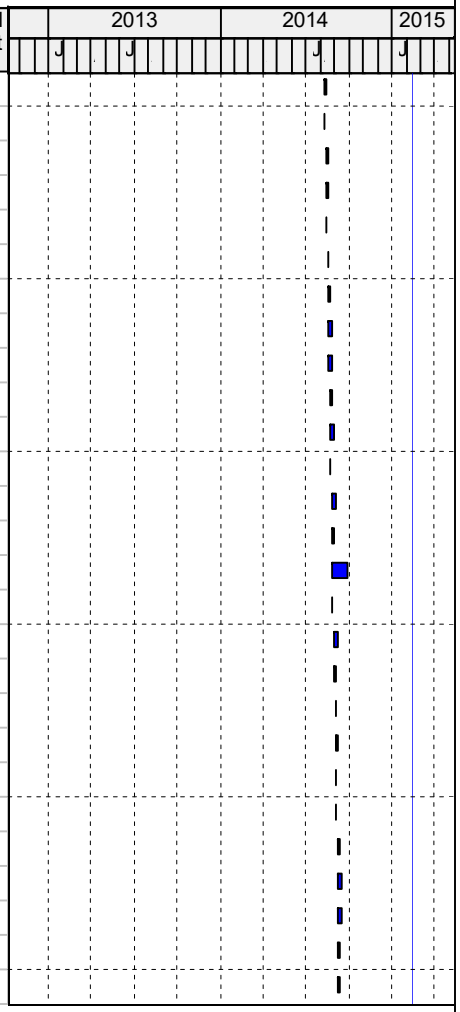



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 08-Sep-14 A | 12-Sep-14 A | |
| L11-8104 | Paint (Prime) | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L04-8116 | Install Base at Guestrooms | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L11-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 10-Sep-14 A | 22-Sep-14 A | |
| L03-8116 | Install Base at Guestrooms | 5 | 0 | 12-Sep-14 A | 16-Sep-14 A | |
| L12-8104 | Paint (Prime) | 2 | 0 | 12-Sep-14 A | 17-Sep-14 A | |
| L05-8116 | Install Base at Guestrooms | 5 | 0 | 16-Sep-14 A | 24-Sep-14 A | |
| L06-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L05-8108 | Elec Trim / Finish | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L07-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 17-Sep-14 A | 23-Sep-14 A | |
| L12-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 17-Sep-14 A | 06-Oct-14 A | |
| L06-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L07-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L14-8104 | Paint (Prime) | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L06-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L06-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L08-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L14-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 24-Sep-14 A | 06-Oct-14 A | |
| L15-8104 | Paint (Prime) | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L03-8110 | HVAC Grilles & Registers | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L03-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8118 | Fire Alarm Trim / Finish | 3 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L10-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 29-Sep-14 A | 01-Oct-14 A | |

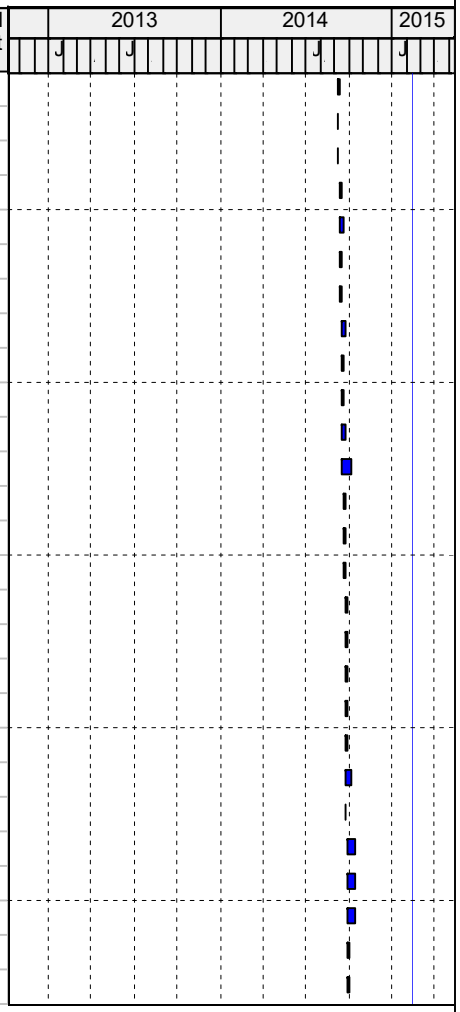


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 30-Sep-14 A | 06-Oct-14 A | |
| L03-8126 | Install Doors | 3 | 0 | 01-Oct-14 A | 07-Oct-14 A | |
| L03-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 01-Oct-14 A | 28-Oct-14 A | |
| L04-8126 | Install Doors | 3 | 0 | 02-Oct-14 A | 09-Oct-14 A | |
| L08-8116 | Install Base at Guestrooms | 5 | 0 | 02-Oct-14 A | 08-Oct-14 A | |
| L04-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8118 | Fire Alarm Trim / Finish | 3 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8108 | Elec Trim / Finish | 4 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L15-8105 | Paint - First Coast & Ceilings | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8126 | Install Doors | 3 | 0 | 08-Oct-14 A | 10-Oct-14 A | |
| L09-8116 | Install Base and Door Thresholds | 5 | 0 | 08-Oct-14 A | 15-Oct-14 A | |
| L09-8124 | Install Flooring | 5 | 0 | 08-Oct-14 A | 14-Oct-14 A | |
| L16-8102S | Stock GWB | 1 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L09-8112 | Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 10-Oct-14 A | |
| L16-8102 | Hang GWB & Inspection | 4 | 0 | 10-Oct-14 A | 17-Oct-14 A | |
| L06-8118 | Fire Alarm Trim / Finish | 3 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L09-8108 | Lighting and Electrical Trim | 3 | 0 | 13-Oct-14 A | 15-Oct-14 A | |
| L10-8124 | Install Flooring | 5 | 0 | 13-Oct-14 A | 16-Oct-14 A | |
| L11-8112 | Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L03-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 14-Oct-14 A | 04-Nov-14 A | |
| L06-8110 | HVAC Grilles & Registers | 2 | 0 | 14-Oct-14 A | 21-Oct-14 A | |
| L06-8126 | Install Doors | 2 | 0 | 14-Oct-14 A | 20-Oct-14 A | |
| L07-8118 | Fire Alarm Trim / Finish | 3 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L12-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L14-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L08-8118 | Fire Alarm Trim / Finish | 3 | 0 | 15-Oct-14 A | 16-Oct-14 A | |

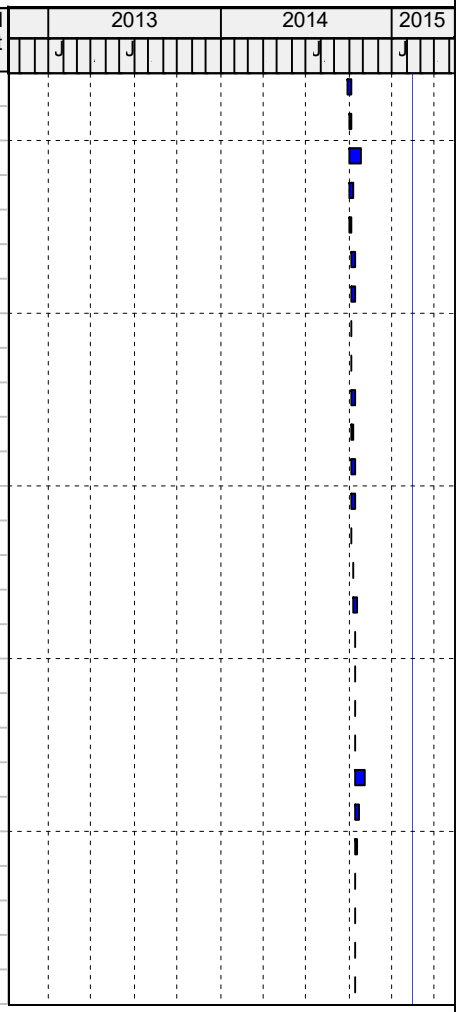



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8116 | Install Base and Door Thresholds | 5 | 0 | 15-Oct-14 A | 23-Oct-14 A | |
| L15-8112 | Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 16-Oct-14 A | |
| L04-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 16-Oct-14 A | 11-Nov-14 A | |
| L11-8124 | Install Flooring | 5 | 0 | 16-Oct-14 A | 22-Oct-14 A | |
| L17-8102S | Stock GWB | 1 | 0 | 17-Oct-14 A | 17-Oct-14 A | |
| L07-8126 | Install Doors | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |
| L09-8118 | Fire Alarm Trim | 2 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| L05-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 21-Oct-14 A | 14-Nov-14 A | |
| L08-8126 | Install Doors | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L10-8118 | Fire Alarm Trim | 2 | 0 | 21-Oct-14 A | 21-Oct-14 A | |
| L09-8126 | Install Doors | 2 | 0 | 22-Oct-14 A | 23-Oct-14 A | |
| L11-8118 | Fire Alarm Trim | 2 | 0 | 22-Oct-14 A | 22-Oct-14 A | |
| L06-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 23-Oct-14 A | 19-Nov-14 A | |
| L10-8126 | Install Doors | 2 | 0 | 23-Oct-14 A | 27-Oct-14 A | |
| L12-8124 | Install Flooring | 5 | 0 | 23-Oct-14 A | 29-Oct-14 A | |
| L12-8118 | Fire Alarm Trim | 2 | 0 | 23-Oct-14 A | 23-Oct-14 A | |
| L11-8116 | Install Base and Door Thresholds | 5 | 0 | 24-Oct-14 A | 26-Nov-14 A | |
| L07-8110 | HVAC Grilles & Registers | 2 | 0 | 27-Oct-14 A | 28-Oct-14 A | |
| L10-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |
| L11-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |
| L17-8102 | Hang GWB & Inspection | 4 | 0 | 27-Oct-14 A | 03-Nov-14 A | |
| L07-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 28-Oct-14 A | 26-Nov-14 A | |
| L08-8120 | Bathrooms - Install Countertops | 3 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L11-8126 | Install Doors | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L12-8108 | Lighting and Electrical Trim | 3 | 0 | 28-Oct-14 A | 30-Oct-14 A | |
| L12-8116 | Install Base and Door Thresholds | 5 | 0 | 28-Oct-14 A | 03-Dec-14 A | |
| L14-8118 | Fire Alarm Trim | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |

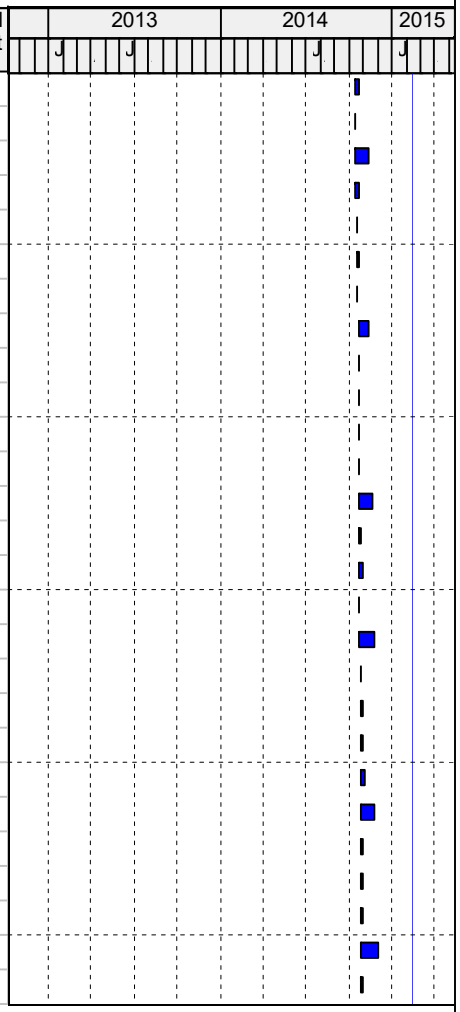



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Oct-14 A | 31-Oct-14 A | |
| L06-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Oct-14 A | 31-Oct-14 A | |
| L12-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L14-8108 | Lighting and Electrical Trim | 3 | 0 | 29-Oct-14 A | 03-Nov-14 A | |
| L14-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8118 | Fire Alarm Trim | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L04-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 30-Oct-14 A | 04-Nov-14 A | |
| L07-8120 | Bathrooms - Install Countertops | 3 | 0 | 03-Nov-14 A | 05-Nov-14 A | |
| L08-8110 | HVAC Grilles & Registers | 2 | 0 | 03-Nov-14 A | 04-Nov-14 A | |
| L09-8120 | Bathrooms - Install Countertops | 3 | 0 | 03-Nov-14 A | 05-Nov-14 A | |
| L10-8120 | Bathrooms - Install Countertops | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| L15-8108 | Lighting and Electrical Trim | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| L11-8120 | Bathrooms - Install Countertops | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| L16-8104 | Paint - Prime | 2 | 0 | 05-Nov-14 A | 06-Nov-14 A | |
| L05-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 07-Nov-14 A | 12-Nov-14 A | |
| L16-8105 | Paint - First Coat & Ceilings | 3 | 0 | 07-Nov-14 A | 11-Nov-14 A | |
| L12-8120 | Bathrooms - Install Countertops | 3 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L14-8124 | Install Flooring | 5 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L06-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 13-Nov-14 A | 17-Nov-14 A | |
| L15-8124 | Install Flooring | 5 | 0 | 17-Nov-14 A | 25-Nov-14 A | |
| L17-8104 | Paint - Prime | 2 | 0 | 17-Nov-14 A | 18-Nov-14 A | |
| L14-8116 | Install Base and Door Thresholds | 5 | 0 | 18-Nov-14 A | 08-Dec-14 A | |
| L16-8126 | Install Doors | 2 | 0 | 18-Nov-14 A | 19-Nov-14 A | |
| L07-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 19-Nov-14 A | 25-Nov-14 A | |
| L15-8116 | Install Base and Door Thresholds | 5 | 0 | 20-Nov-14 A | 08-Dec-14 A | |
| L03-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |

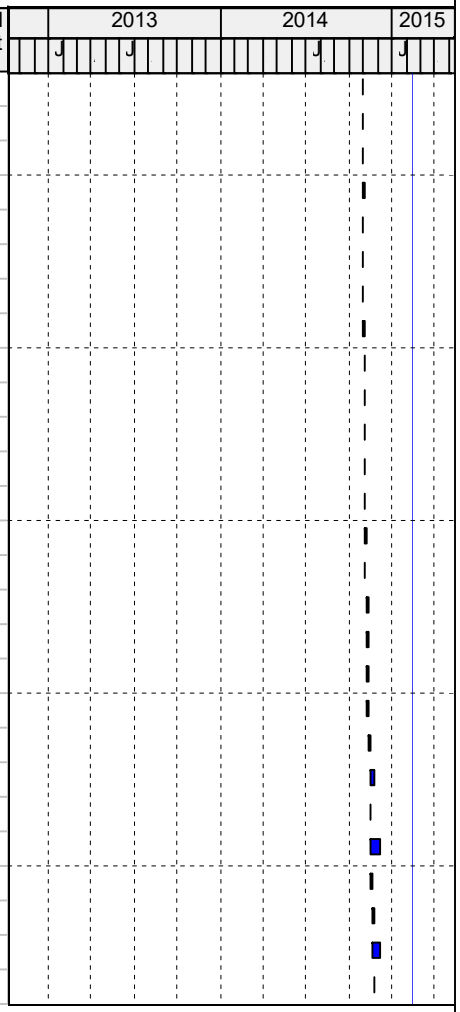



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L05-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L08-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| L17-8105 | Paint - First Coat & Ceilings | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L16-8124 | Install Flooring | 5 | 0 | 25-Nov-14 A | 03-Dec-14 A | |
| L16-8112 | Fire Sprinkler Trim | 2 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| L16-8118 | Fire Alarm Trim | 2 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| L06-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L07-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L08-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 01-Dec-14 A | 08-Dec-14 A | |
| L08-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L09-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 01-Dec-14 A | 10-Dec-14 A | |
| L16-8108 | Lighting and Electrical Trim | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L17-8126 | Install Doors | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| L16-8116 | Install Base and Door Thresholds | 5 | 0 | 02-Dec-14 A | 15-Dec-14 A | |
| L17-8112 | Fire Sprinkler Trim | 2 | 0 | 02-Dec-14 A | 02-Dec-14 A | |
| L09-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 03-Dec-14 A | 08-Dec-14 A | |
| L09-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L10-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L11-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L17-8118 | Fire Alarm Trim | 2 | 0 | 03-Dec-14 A | 03-Dec-14 A | |
| L12-8107 | Paint Final Coat | 3 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L14-8120 | Bathrooms - Install Countertops | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L17-8108 | Lighting and Electrical Trim | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L10-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L15-8120 | Bathrooms - Install Countertops | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 10-Dec-14 A | 16-Dec-14 A | |

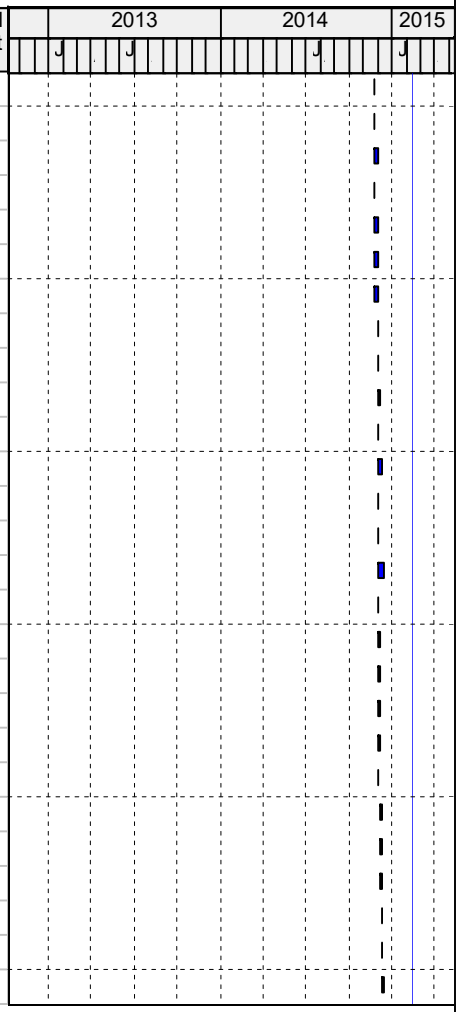


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 10-Dec-14 A | 24-Dec-14 A | |
| L04-8132 | Contractor Punchlist (inspect/distribute/correct/back-pl | 7 | 0 | 11-Dec-14 A | 05-Feb-15 A | |
| L04-8134 | Final Clean @ Guestrooms | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L05-8132 | Contractor Punchlist (inspect/distribute/correct/back-pl | 7 | 0 | 12-Dec-14 A | 10-Feb-15 A | |
| L05-8134 | Final Clean @ Guestrooms | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L11-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 12-Dec-14 A | 17-Dec-14 A | |
| L06-8134 | Final Clean @ Guestrooms | 5 | 0 | 13-Dec-14 A | 13-Dec-14 A | |
| L12-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 15-Dec-14 A | 18-Dec-14 A | |
| L17-8124 | Install Flooring | 5 | 0 | 15-Dec-14 A | 18-Dec-14 A | |
| L17-8116 | Install Base and Door Thresholds | 5 | 0 | 18-Dec-14 A | 30-Dec-14 A | |
| L12-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| L14-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| L15-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 29-Dec-14 A | 05-Jan-15 A | |
| L16-8120 | Bathrooms - Install countertops | 3 | 0 | 29-Dec-14 A | 09-Jan-15 A | |
| L14-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 30-Dec-14 A | 05-Jan-15 A | |
| L15-8122 | Bathrooms - Plumbing fixtures & trim | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L16-8128 | Bathrooms - Install shower/tub surrounds | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L16-8122 | Bathrooms - Plumbing fixtures & trim | 3 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8128 | Bathrooms - Install shower/tub surrounds | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L09-8110 | HVAC grilles & registers | 2 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| L11-8110 | HVAC grilles & registers | 2 | 0 | 21-Jan-15 A | 28-Jan-15 A | |
| L12-8110 | HVAC grilles & registers | 2 | 0 | 21-Jan-15 A | 28-Jan-15 A | |
| L14-8110 | HVAC grilles & registers | 2 | 0 | 21-Jan-15 A | 02-Feb-15 A | |
| L10-8110 | HVAC grilles & registers | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L15-8110 | HVAC grilles & registers | 2 | 1 | 03-Feb-15 A | 16-Feb-15 | 25 |
| L16-8110 | HVAC grilles & registers | 2 | 1 | 03-Feb-15 A | 16-Feb-15 | 27 |
| L17-8122 | Bathrooms - Plumbing fixtures & trim | 3 | 1 | 03-Feb-15 A | 17-Feb-15 | 30 |

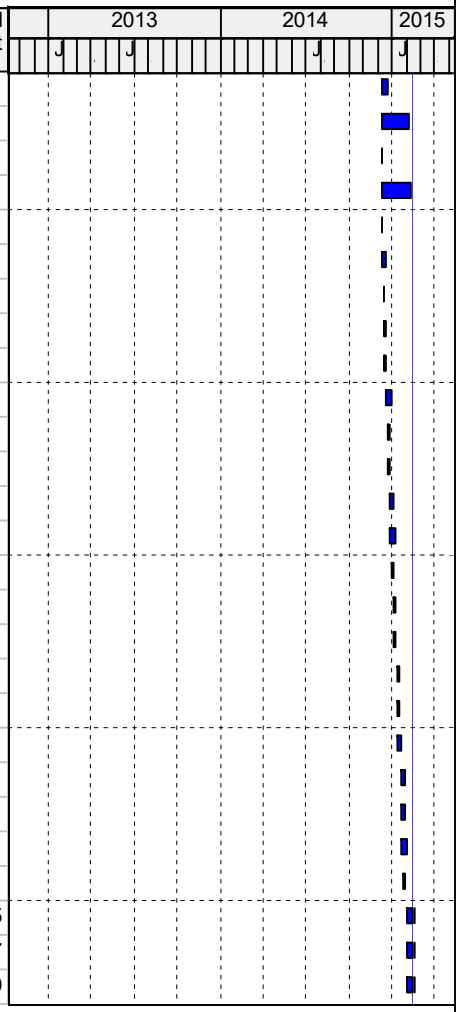


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8120 | Bathrooms - Install countertops | 3 | 1 | 03-Feb-15 A | 16-Feb-15 | 26 |
| L06-8132 | Contractor Punchlist (inspect/distribute/correct/back-pı | 7 | 0 | 04-Feb-15 A | 12-Feb-15 A | |
| L07-8132 | Contractor Punchlist (inspect/distribute/correct/back-pı | 7 | 1 | 06-Feb-15 A | 16-Feb-15 | 13 |
| L14-8107 | Paint, final coat & touch-up | 3 | 0 | 09-Feb-15 A | 11-Feb-15 A | |
| L17-8110 | HVAC grilles & registers | 2 | 1 | 09-Feb-15 A | 17-Feb-15 | 26 |
| L08-8132 | Contractor Punchlist (inspect/distribute/correct/back-pı | 7 | 3 | 10-Feb-15 A | 18-Feb-15 | 13 |
| L09-8132 | Contractor Punchlist (inspect/distribute/correct/back-pı | 7 | 5 | 12-Feb-15 A | 20-Feb-15 | 13 |
| L03-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 23 |
| L04-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 18 |
| L05-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 16 |
| L06-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 16 |
| L07-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 13 |
| L08-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 15 |
| L09-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 13 |
| L10-8132 | Contractor Punchlist (inspect/distribute/correct/back-pı | 7 | 7 | 16-Feb-15 | 24-Feb-15 | 13 |
| L10-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 15 |
| L11-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 14 |
| L12-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 16 |
| L14-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 24 |
| L15-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 24 |
| L16-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 16-Feb-15 | 16-Feb-15 | 24 |
| L15-8107 | Paint, final coat & touch-up | 3 | 3 | 17-Feb-15 | 19-Feb-15 | 25 |
| L16-8107 | Paint, final coat & touch-up | 3 | 3 | 17-Feb-15 | 19-Feb-15 | 27 |
| L17-8109 | Acoustical ceiling tile at corridors | 1 | 1 | 17-Feb-15 | 17-Feb-15 | 23 |
| L11-8132 | Contractor Punchlist (inspect/distribute/correct/back-pı | 7 | 7 | 18-Feb-15 | 26-Feb-15 | 13 |
| L17-8107 | Paint, final coat & touch-up | 3 | 3 | 18-Feb-15 | 20-Feb-15 | 26 |
| L12-8132 | Contractor Punchlist (inspect/distribute/correct/back-pı | 7 | 7 | 20-Feb-15 | 02-Mar-15 | 13 |

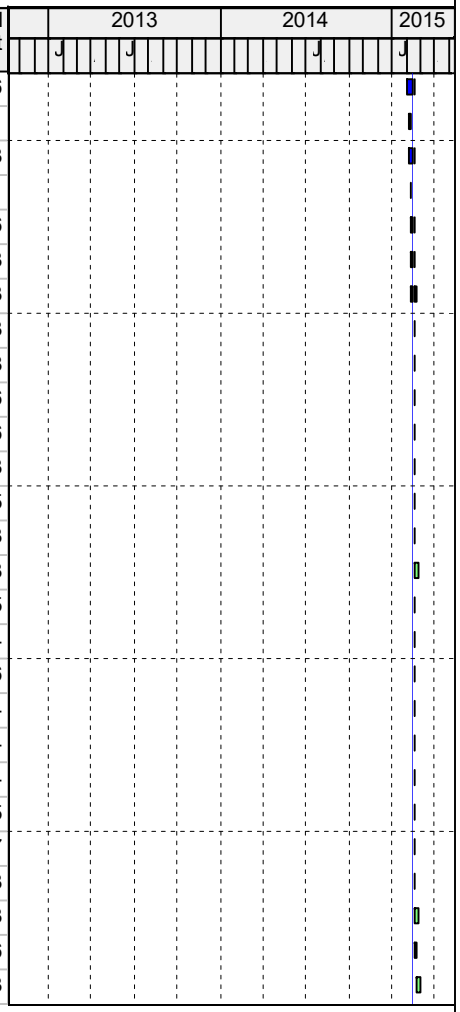


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 7 | 24-Feb-15 | 04-Mar-15 | 27 |
| L14-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 7 | 24-Feb-15 | 04-Mar-15 | 21 |
| L15-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 7 | 26-Feb-15 | 06-Mar-15 | 21 |
| L16-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 7 | 02-Mar-15 | 10-Mar-15 | 21 |
| L17-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 7 | 04-Mar-15 | 12-Mar-15 | 21 |
| **Pool Area** | | | | | | |
| L03-8216 | Install pool tile, coping and depth markers | 5 | 5 | 16-Mar-15 | 20-Mar-15 | 2 |
| **Corridors / Common / Public Areas** | | | | | | |
| L03-8200 | Vinyl Wall Coverings | 3 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L04-8200 | Vinyl Wall Coverings | 5 | 0 | 06-Aug-14 A | 12-Aug-14 A | |
| L05-8200 | Vinyl Wall Coverings | 5 | 0 | 12-Aug-14 A | 22-Sep-14 A | |
| L03-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L06-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L08-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 11-Sep-14 A | 19-Sep-14 A | |
| L04-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| L05-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L06-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L07-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L09-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| L10-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 08-Oct-14 A | |
| L11-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 10-Oct-14 A | |
| L08-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L12-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| L09-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L14-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 16-Oct-14 A | 27-Oct-14 A | |
| L10-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |

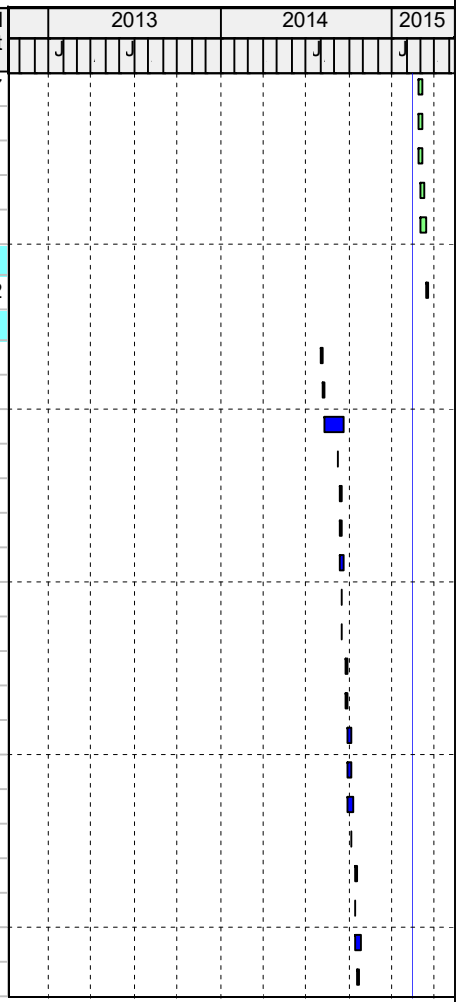



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L15-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 22-Oct-14 A | 29-Oct-14 A | |
| L12-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 03-Nov-14 A | 04-Nov-14 A | |
| L14-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L15-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 05-Nov-14 A | 06-Nov-14 A | |
| L16-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 14-Nov-14 A | 20-Nov-14 A | |
| L16-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L17-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L17-8200 | Wall coverings - vinyl at window niches & outside bath | 4 | 1 | 15-Dec-14 A | 16-Feb-15 | 18 |
| L04-8206 | Flooring - carpet at corridors | 2 | 0 | 14-Jan-15 A | 23-Jan-15 A | |
| L05-8206 | Flooring - carpet at corridors | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| L07-8206 | Flooring - carpet at corridors | 2 | 0 | 22-Jan-15 A | 23-Jan-15 A | |
| L06-8206 | Flooring - carpet at corridors | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L09-8206 | Flooring - carpet at corridors | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| L08-8206 | Flooring - carpet at corridors | 2 | 0 | 04-Feb-15 A | 05-Feb-15 A | |
| L10-8206 | Flooring - carpet at corridors | 2 | 0 | 06-Feb-15 A | 09-Feb-15 A | |
| L11-8206 | Flooring - carpet at corridors | 2 | 0 | 10-Feb-15 A | 11-Feb-15 A | |
| L12-8206 | Flooring - carpet at corridors | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| L14-8206 | Flooring - carpet at corridors | 2 | 0 | 13-Feb-15 A | 14-Feb-15 A | |
| L04-8210 | Owner Punchlist (inspect/distribute/correct/back-punch | 5 | 5 | 16-Feb-15 | 20-Feb-15 | 17 |
| L15-8206 | Flooring - carpet at corridors | 2 | 2 | 16-Feb-15 | 17-Feb-15 | 27 |
| L05-8210 | Owner Punchlist (inspect/distribute/correct/back-punch | 5 | 5 | 17-Feb-15 | 24-Feb-15 | 16 |
| L06-8210 | Owner Punchlist (inspect/distribute/correct/back-punch | 5 | 5 | 17-Feb-15 | 23-Feb-15 | 16 |
| L07-8210 | Owner Punchlist (inspect/distribute/correct/back-punch | 5 | 5 | 17-Feb-15 | 23-Feb-15 | 16 |
| L16-8206 | Flooring - carpet at corridors | 2 | 2 | 18-Feb-15 | 19-Feb-15 | 27 |
| L08-8210 | Owner Punchlist (inspect/distribute/correct/back-punch | 5 | 5 | 19-Feb-15 | 25-Feb-15 | 14 |
| L04-8208 | Final Cleaning | 2 | 2 | 20-Feb-15 | 23-Feb-15 | 17 |

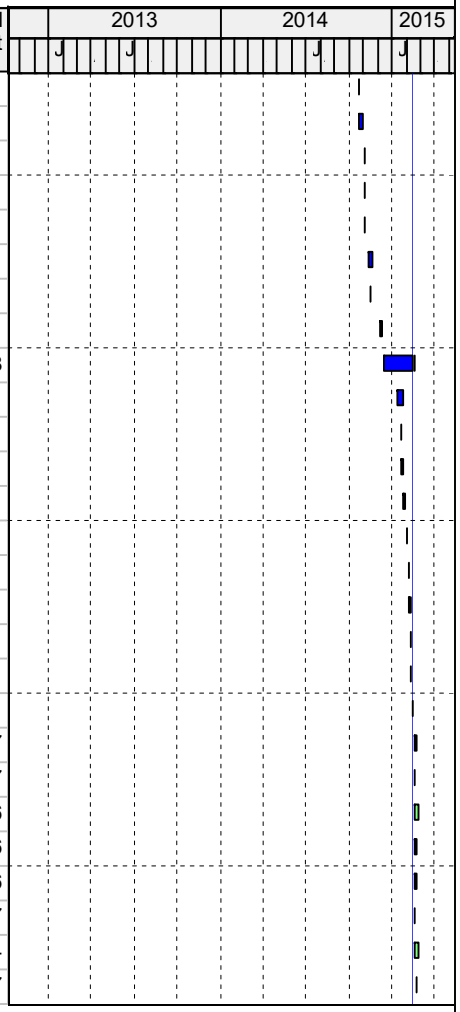


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8208 | Final Cleaning | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 16 |
| L07-8208 | Final Cleaning | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 16 |
| L09-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 23-Feb-15 | 27-Feb-15 | 13 |
| L17-8206 | Flooring - carpet at corridors | 2 | 2 | 23-Feb-15 | 24-Feb-15 | 26 |
| L05-8208 | Final Cleaning | 2 | 2 | 23-Feb-15 | 25-Feb-15 | 16 |
| L04-8214 | Floor Complete | 0 | 0 | | 23-Feb-15 | 17 |
| L06-8214 | Floor Complete | 0 | 0 | | 24-Feb-15 | 16 |
| L07-8214 | Floor Complete | 0 | 0 | | 24-Feb-15 | 16 |
| L08-8208 | Final Cleaning | 2 | 2 | 25-Feb-15 | 26-Feb-15 | 14 |
| L10-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 25-Feb-15 | 03-Mar-15 | 33 |
| L05-8214 | Floor Complete | 0 | 0 | | 25-Feb-15 | 16 |
| L08-8214 | Floor Complete | 0 | 0 | | 26-Feb-15 | 14 |
| L09-8208 | Final Cleaning | 2 | 2 | 27-Feb-15 | 02-Mar-15 | 13 |
| L11-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 27-Feb-15 | 05-Mar-15 | 31 |
| L09-8214 | Floor Complete | 0 | 0 | | 02-Mar-15 | 13 |
| L10-8208 | Final Cleaning | 2 | 2 | 03-Mar-15 | 04-Mar-15 | 33 |
| L12-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 03-Mar-15 | 09-Mar-15 | 29 |
| L10-8214 | Floor Complete | 0 | 0 | | 04-Mar-15 | 33 |
| L03-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 05-Mar-15 | 11-Mar-15 | 27 |
| L11-8208 | Final Cleaning | 2 | 2 | 05-Mar-15 | 06-Mar-15 | 31 |
| L14-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 05-Mar-15 | 11-Mar-15 | 27 |
| L11-8214 | Floor Complete | 0 | 0 | | 06-Mar-15 | 31 |
| L12-8208 | Final Cleaning | 2 | 2 | 09-Mar-15 | 10-Mar-15 | 29 |
| L15-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 09-Mar-15 | 13-Mar-15 | 25 |
| L12-8214 | Floor Complete | 0 | 0 | | 10-Mar-15 | 29 |
| L03-8208 | Final Cleaning | 2 | 2 | 11-Mar-15 | 12-Mar-15 | 27 |
| L14-8208 | Final Cleaning | 2 | 2 | 11-Mar-15 | 12-Mar-15 | 27 |

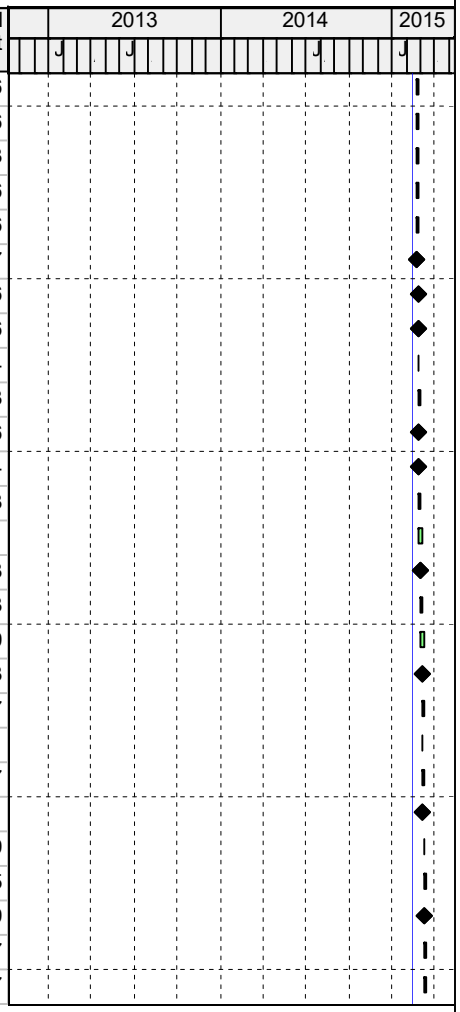



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 11-Mar-15 | 17-Mar-15 | 23 |
| L14-8214 | Floor Complete | 0 | 0 | | 12-Mar-15 | 27 |
| L15-8208 | Final Cleaning | 2 | 2 | 13-Mar-15 | 16-Mar-15 | 25 |
| L17-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 13-Mar-15 | 19-Mar-15 | 21 |
| L15-8214 | Floor Complete | 0 | 0 | | 16-Mar-15 | 25 |
| L16-8208 | Final Cleaning | 2 | 2 | 17-Mar-15 | 18-Mar-15 | 23 |
| L16-8214 | Floor Complete | 0 | 0 | | 18-Mar-15 | 23 |
| L17-8208 | Final Cleaning | 2 | 2 | 19-Mar-15 | 20-Mar-15 | 21 |
| L17-8214 | Floor Complete | 0 | 0 | | 20-Mar-15 | 21 |
| L03-8206 | Flooring - carpet at corridors | 2 | 2 | 02-Apr-15 | 03-Apr-15 | 2 |
| L03-8214 | Floor Complete | 0 | 0 | | 16-Apr-15 | 2 |
| **Mech Penthouse** | | | | | | |
| PH-8100 | PH - Insulation & Vapor Barrier | 5 | 0 | 09-Oct-14 A | 13-Oct-14 A | |
| PH-8102 | PH - Complete GWB Hang / Tape / Finish | 6 | 0 | 14-Oct-14 A | 10-Nov-14 A | |
| PH-8122 | PH - Plumbing Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8110 | PH - HVAC Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8126 | PH - install doors & hardware | 2 | 1 | 24-Nov-14 A | 16-Feb-15 | 40 |
| PH-8104 | PH - Int Painting [DELETED] | 4 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| PH-8108 | PH - Elec Trim / Finish | 5 | 0 | 01-Dec-14 A | 19-Jan-15 A | |
| PH-8114 | PH - Install Stairs to Roof [DELETED] | 1 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| PH-8118 | PH - Fire Alarm Trim (speaker/strobe & smoke detecto | 5 | 0 | 01-Dec-14 A | 21-Jan-15 A | |
| PH-8124 | PH - Flooring [DELETED, NIC] | 5 | 0 | 01-Jan-15 A | 01-Jan-15 A | |
| PH-8132 | PH - Contractor Pre-Punchlist | 1 | 1 | 17-Feb-15 | 17-Feb-15 | 42 |
| PH-8134 | PH - Final Trims and Touch-Up | 3 | 3 | 17-Feb-15 | 19-Feb-15 | 40 |
| PH-8208 | PH - Final Clean | 1 | 1 | 20-Feb-15 | 20-Feb-15 | 40 |
| PH-8212 | PH - Final Punchlist | 1 | 1 | 23-Feb-15 | 23-Feb-15 | 40 |

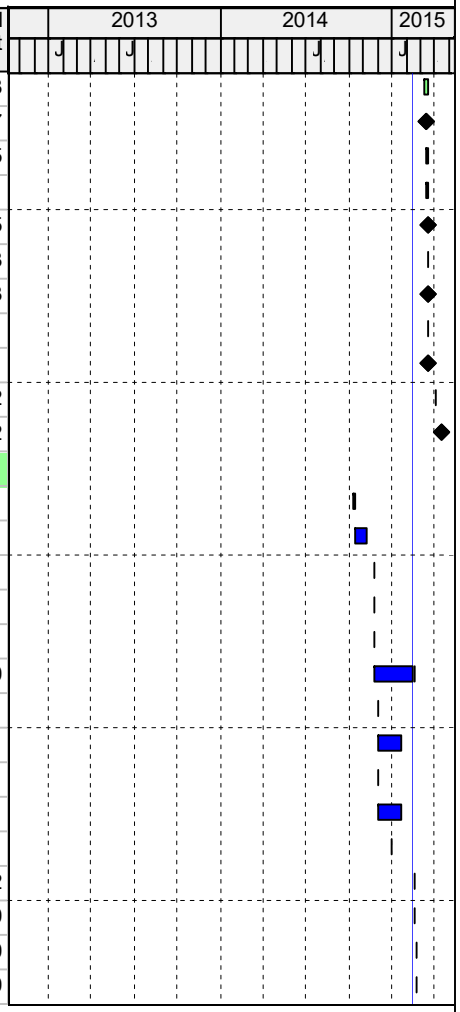


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-8214 | PH - Floor Complete | 0 | 0 | | 23-Feb-15 | 40 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| Smoke Control | | | | | | |
| CO-7104 | Smoke Control Pre-Testing (Podium) | 5 | 5 | 07-Apr-15 | 13-Apr-15 | 10 |
| CO-7106 | City of Bellevue Smoke Control Testing (Podium) | 5 | 5 | 16-Apr-15 | 22-Apr-15 | 8 |
| CO-7108 | Final Marriott Smoke Control Testing | 2 | 2 | 01-May-15 | 05-May-15 | 2 |
| Fire Sprinklers | | | | | | |
| CO-7110 | Fire Sprinkler Pre-Testing (Podium) | 5 | 5 | 31-Mar-15 | 06-Apr-15 | 10 |
| CO-7112 | City of Bellevue Fire Sprinkler Inspection / Approval (F | 5 | 5 | 16-Apr-15 | 22-Apr-15 | 8 |
| CO-7114 | Marriott Fire Sprinkler Testing | 2 | 2 | 01-May-15 | 05-May-15 | 2 |
| Fire Alarm | | | | | | |
| CO-7116 | Fire Alarm Pre-Testing (Podium) | 5 | 5 | 31-Mar-15 | 06-Apr-15 | 10 |
| CO-7118 | City of Bellevue Fire Alarm Inspection / Approval (Pod | 5 | 5 | 16-Apr-15 | 22-Apr-15 | 8 |
| CO-7120 | Marriott Fire Alarm Testing | 2 | 2 | 01-May-15 | 05-May-15 | 2 |
| Start-Up / Testing / Commissioning | | | | | | |
| CO-7100 | Cx - Start-Up - Garage Exhaust Fan and VFD's | 4 | 4 | 16-Feb-15* | 19-Feb-15 | 23 |
| CO-7102 | Cx - DDC Point-To-Point - Garage Exhaust Fans | 5 | 5 | 20-Feb-15 | 26-Feb-15 | 47 |

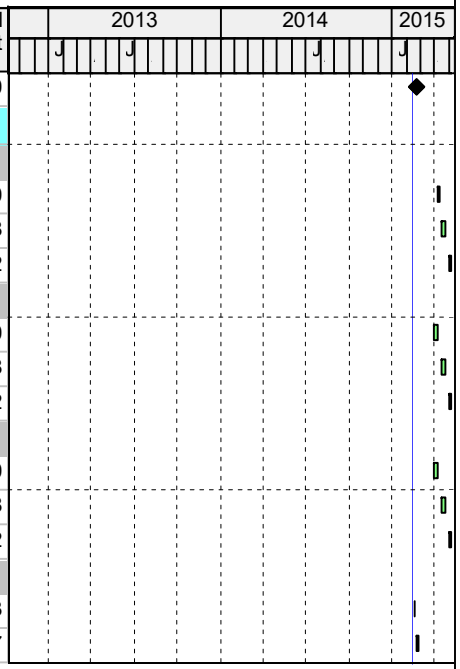



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Working Schedule - 3-16-15 Update** | | | | | | |
| L09-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-04 A | 30-Sep-14 A | |
| I-4500 | Re-design building exterior (change from EIFS panels | 30 | 0 | 12-Apr-13 A | 28-May-14 A | |
| ASI01 | ASI No. 1 - Tower Crane Foundation Changes | 0 | 0 | 09-May-13 A | | |
| I-2292 | RFI 233/ Original HVAC submittal with specified damp | 1 | 0 | 13-May-13 A | 12-Jun-13 A | |
| ASI03 | ASI No. 3 - Food Service Plans and Cut Sheets | 0 | 0 | 14-May-13 A | | |
| ASI04 | ASI No. 4 - Revised Structural For The Podium | 0 | 0 | 22-May-13 A | | |
| ASI05 | ASI No. 5 - NTI Drawings | 0 | 0 | 22-May-13 A | | |
| I-1500 | Owner release revised LV design - Tower (ASIs 5, 13, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-1550 | Owner release revised LV design - Podium (ASIs 5, 1 | 200 | 0 | 23-May-13 A | 28-Apr-14 A | |
| I-1900 | Owner issue design revisions (ASIs 4, 9, 19, 34) | 215 | 0 | 23-May-13 A | 24-Mar-14 A | |
| I-2500 | Owner issue LL1 electrical revisions (ASIs 7, 9r2, 14, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| ASI02 | ASI No. 2 - Foundation Drainage System | 0 | 0 | 05-Jun-13 A | | |
| ASI04c | ASI No. 4 - Revised Structural For The Podium (Cloud | 0 | 0 | 05-Jun-13 A | | |
| ASI07 | ASI No. 7 - Electrical Rev-10 Changes | 0 | 0 | 18-Jun-13 A | | |
| ASI06 | ASI No. 6 - Mechanical Rev-8 Changes | 0 | 0 | 19-Jun-13 A | | |
| I-3700 | Owner resolve wall condition between stair and Eleva | 200 | 0 | 27-Jun-13 A | 16-Jun-14 A | |
| MM-1000 | MM - Temporary Power Available | 0 | 0 | 08-Jul-13 A | | |
| I-2100 | Owner revise roof steel design (Submittals 365, 370, | 200 | 0 | 09-Jul-13 A | 07-Apr-14 A | |
| I-2200 | Owner resolve elevator steel issue (RFI 112, RFI 112. | 200 | 0 | 09-Jul-13 A | 03-Mar-14 A | |
| I-2400 | Owner provide Tower light fixture selections (ASI 36) | 185 | 0 | 18-Jul-13 A | 08-Apr-14 A | |
| I-3400 | Owner provide Level 2 ceiling heights (RFI 465) | 180 | 0 | 19-Jul-13 A | 01-Jul-14 A | |
| I-2294 | RFI 233/ Revised HVAC submittal | 1 | 0 | 22-Jul-13 A | 25-Jul-13 A | |
| ASI04ca | ASI No. 4 - Revised Structural For The Podium (City A | 0 | 0 | 05-Aug-13 A | | |
| ASI11 | ASI No. 11 - Food and Beverage Drawing Revisions | 0 | 0 | 05-Aug-13 A | | |
| I-2900 | Owner revise Food Service and Kitchen (ASIs 11, 12, | 140 | 0 | 08-Aug-13 A | 27-Feb-14 A | |
| ASI12 | ASI No. 12 - Food and Beverage Drawing Changes | 0 | 0 | 12-Aug-13 A | | |

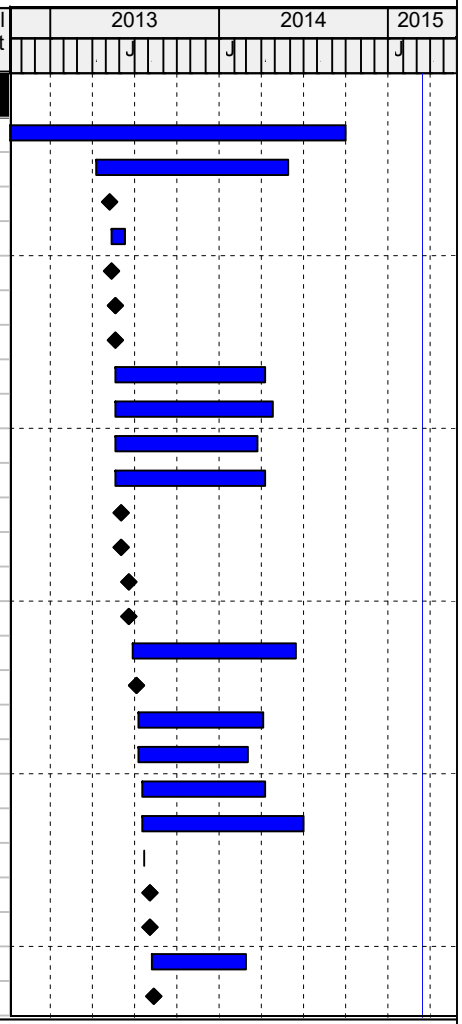


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| High Rise Hotel Sample Project | All Activities | Schedule Status Date 16-Mar-15 |
|---|---|---|

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ASI08 | ASI No. 8 - Provent System | 0 | 0 | 15-Aug-13 A | | |
| I-5010 | RFI 173 - Porte Cochere Bench Design | 1 | 0 | 16-Aug-13 A | 04-Sep-13 A | |
| I-5012 | RFI 189 - Porte Cochere Pavement Design | 1 | 0 | 26-Aug-13 A | 30-Jun-14 A | |
| I-1400 | Owner develop envelope redesign | 70 | 0 | 27-Aug-13 A | 12-Dec-13 A | |
| I-5014 | RFI 197 - LL1 & LL2 Planter Drain Pipes | 1 | 0 | 03-Sep-13 A | 06-Sep-13 A | |
| I-3600 | Owner closeout glass/glazing allowance | 160 | 0 | 04-Sep-13 A | 30-Apr-14 A | |
| ASI09 | ASI No. 9 - Incorporating Arch, MEP & Struct Drawing | 0 | 0 | 05-Sep-13 A | | |
| I-1200 | Owner release revised Concierge Lounge design (AS | 160 | 0 | 06-Sep-13 A | 22-Oct-14 A | |
| ASI13 | ASI No. 13 - NTI Drawing Updates | 0 | 0 | 06-Sep-13 A | | |
| I-2800 | Owner revise interior public space design (ASIs 16, 1 | 130 | 0 | 25-Sep-13 A | 09-Apr-14 A | |
| ASI16 | ASI No. 16 - 9.20..13 General ID Releasae | 0 | 0 | 25-Sep-13 A | | |
| I-2296 | RFI 233/ Issue RFI and receive response | 1 | 0 | 25-Sep-13 A | 21-Jan-14 A | |
| I-2000 | Owner approve door frames (Submittals 258, 454, 4 | 85 | 0 | 27-Sep-13 A | 23-Jan-14 A | |
| ASI14 | ASI No. 14 - Electrical Revisions for Low Voltage | 0 | 0 | 04-Oct-13 A | | |
| ASI17 | ASI No. 17 - Smoke Control Design 42C Permit | 0 | 0 | 09-Oct-13 A | | |
| ASI18 | ASI No. 18 - Interior Package Revisions | 0 | 0 | 15-Oct-13 A | | |
| I-3100 | Owner revise ballroom ceiling design (ASIs 18, 25) | 100 | 0 | 17-Oct-13 A | 25-Feb-14 A | |
| I-1600 | Owner provide directive for south & east corridor encl | 110 | 0 | 28-Oct-13 A | 18-Apr-14 A | |
| I-5016 | RFI 282 - Porte Cochere Planter Dimensions | 1 | 0 | 01-Nov-13 A | 21-Jan-14 A | |
| ASI11-12 | ASI No. 11 & 12 - Kitchen Equipment Specifications | 0 | 0 | 06-Nov-13 A | | |
| ASI09r1s | ASI No. 9 (Revised) - City Approved ASI No. 9 (Struct | 0 | 0 | 07-Nov-13 A | | |
| I-2600 | Owner resolve L2 slab coordination issue | 4 | 0 | 13-Nov-13 A | 16-Nov-13 A | |
| ASI09r1m | ASI No. 9 (Revised) - City Approved ASI No. 9 (Mecha | 0 | 0 | 15-Nov-13 A | | |
| ASI06r1 | ASI No. 6 (Revised) - Mechanical Rev-8 Changes (Cit | 0 | 0 | 19-Nov-13 A | | |
| ASI21 | ASI No. 21 - Revised Structural Drawings for the Roof | 0 | 0 | 22-Nov-13 A | | |
| I-2700 | Owner revise tower guest rooms design (ASIs 23, 29) | 58 | 0 | 04-Dec-13 A | 26-Feb-14 A | |
| ASI09r1e | ASI No. 9 (Revised) - ASI No. 9 Electrical Drawings (R | 0 | 0 | 04-Dec-13 A | | |

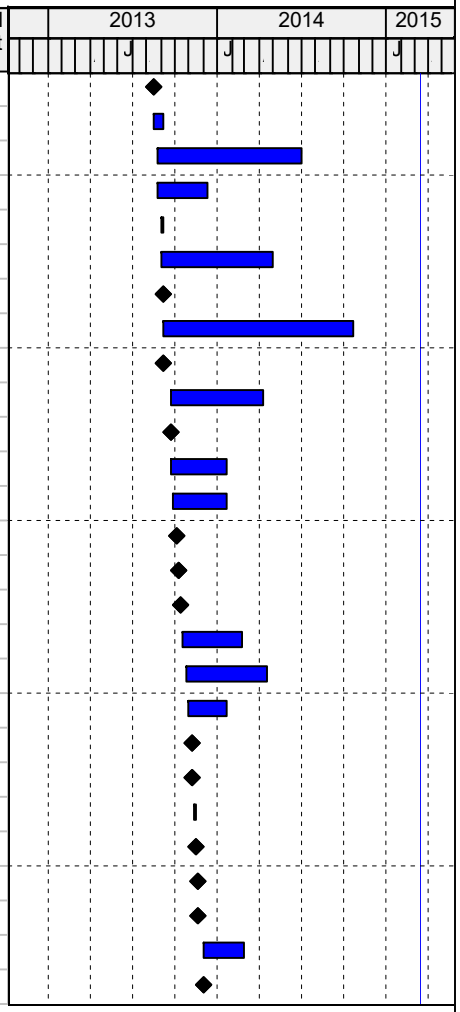


Actual Work
Remaining Work
Critical Remai...
Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ASI20 | ASI No. 20 - Dry Utilities Revisions | 0 | 0 | 05-Dec-13 A | | |
| I-1700 | Owner provide design for dry site utilities (ASIs 20, 20 | 66 | 0 | 09-Dec-13 A | 13-Mar-14 A | |
| I-1402 | Begin exterior panel production | 41 | 0 | 13-Dec-13 A | 12-Feb-14 A | |
| ASI17ca | ASI No. 17 - Smoke Control Design 42C Permit (City / | 0 | 0 | 16-Dec-13 A | | |
| ASI09r2e | ASI No. 9 (Revised) - ASI No. 9 Electrical Drawings (R | 0 | 0 | 18-Dec-13 A | | |
| I-1300 | Owner issue "Hold" directive (email) | 0 | 0 | | 19-Dec-13 A | |
| ASI22 | ASI No. 22 - Revised Door Schedule and Door Hardw | 0 | 0 | 19-Dec-13 A | | |
| I-1100 | Owner release revised L17 design (ASI 23, 29R1) | 74 | 0 | 20-Dec-13 A | 08-Apr-14 A | |
| I-1302 | Owner issue ASI 30 (Prep Kitchen Revisions) | 47 | 0 | 20-Dec-13 A | 27-Feb-14 A | |
| ASI23 | ASI No. 23 - Revised Tower and Enlarged Guestroom | 0 | 0 | 20-Dec-13 A | | |
| I-1404 | City of Bellevue Approval | 90 | 0 | 23-Dec-13 A | 15-Jul-14 A | |
| I-5470 | Resolve ceiling height issue at Laundy Room (RFI __ | 5 | 0 | 05-Jan-14 A | 30-Jan-15 A | |
| ASI15 | ASI No. 15 - NTI DV Drawings Revisions | 0 | 0 | 08-Jan-14 A | | |
| ASI09R2e2 | ASI No. 9 (Revised) - City Approved ASI No. 9 (Electri | 0 | 0 | 14-Jan-14 A | | |
| ASI22r1 | ASI No. 22 (Revised) - Architectural Revisions to Door | 0 | 0 | 20-Jan-14 A | | |
| I-3000 | ASI 38/ Owner revise bar area (change to straight bai | 71 | 0 | 22-Jan-14 A | 27-May-14 A | |
| I-2298 | RFI 233/ Resolve issue with designer & City | 1 | 0 | 22-Jan-14 A | 14-Mar-14 A | |
| ASI20r1 | ASI No. 20 (Revised) - Dry Utilities Revsions | 0 | 0 | 23-Jan-14 A | | |
| ASI24 | ASI No. 24 - FRCH ID Finish Schedule | 0 | 0 | 30-Jan-14 A | | |
| ASI26 | ASI No. 26 - Revised Laundry Layout and Equipment | 0 | 0 | 12-Feb-14 A | | |
| I-1306 | Prep Kitchen - Additional plumbing (ASI 30) | 4 | 0 | 17-Feb-14 A | 01-Aug-14 A | |
| ASI28 | ASI No. 28 - Guest Laundry Equipment Sheets | 0 | 0 | 20-Feb-14 A | | |
| ASI27 | ASI No. 27 - Mechanical, Electrical and Plumbing She | 0 | 0 | 21-Feb-14 A | | |
| ASI25 | ASI No. 25 - Podium Level Revisions (Stair 1 & 2 Gat | 0 | 0 | 24-Feb-14 A | | |
| ASI29 | ASI No. 29 - Architectural Tower and Guestroom Revi | 0 | 0 | 26-Feb-14 A | | |
| ASI30 | ASI No. 30 - Food Service Revisions per HEI | 0 | 0 | 27-Feb-14 A | | |
| I-2202 | Fabricate revised elevator steel | 60 | 0 | 04-Mar-14 A | 07-May-14 A | |

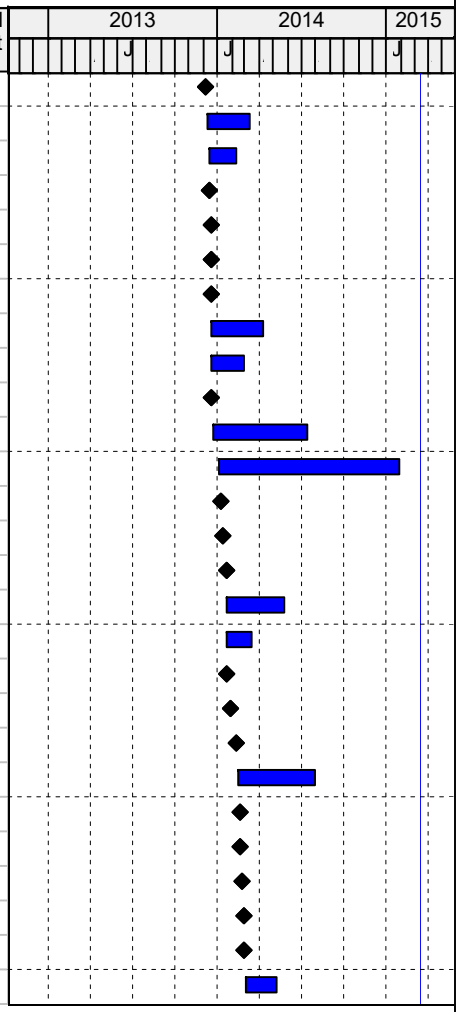


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-2704 | Framing "Go Back" work for ASIs 23, 29 - L4 | 1 | 0 | 05-Mar-14 A | 12-Mar-14 A | |
| ASI31 | ASI No. 31 - Revised Elevations | 0 | 0 | 07-Mar-14 A | | |
| ASI33 | ASI No. 33 - NTI DV Drawing Revisions | 0 | 0 | 11-Mar-14 A | | |
| ASI20r2 | ASI No. 20 (Revised) - Dry Utilities Revisions | 0 | 0 | 13-Mar-14 A | | |
| I-1702 | Owner provide directive to proceed | 26 | 0 | 14-Mar-14 A | 01-May-14 A | |
| I-2300 | RFI 233/ Procure dampers | 1 | 0 | 15-Mar-14 A | 11-Apr-14 A | |
| I-3300 | Owner provide Guest Room plumbing fixture selectio | 1 | 0 | 20-Mar-14 A | 20-Mar-14 A | |
| ASI34 | ASI No. 34 - SCA Structural Revisions S6.01 and S6.( | 0 | 0 | 24-Mar-14 A | | |
| I-4600 | RFI 72, HHP3-HHP5 - resolve electrical issue & revise | 1 | 0 | 24-Mar-14 A | 09-Apr-14 A | |
| I-1902 | Procure revised structural steel | 15 | 0 | 25-Mar-14 A | 14-Apr-14 A | |
| I-3900 | Ballroom Parapet Height Issue/ RFI 471 | 1 | 0 | 28-Mar-14 A | 07-May-14 A | |
| I-3016 | ASI 38/ Scan Level 1 slab at bar (3 times) | 1 | 0 | 31-Mar-14 A | 11-Apr-14 A | |
| I-4000 | Owner complete design of east stitched enclosure (fo | 1 | 0 | 01-Apr-14 A | 14-May-14 A | |
| ASI35 | ASI No. 35 - FRCH ID Revisions and Finish Schedule | 0 | 0 | 07-Apr-14 A | | |
| I-2102 | Fabricate revised roof steel | 20 | 0 | 08-Apr-14 A | 15-May-14 A | |
| I-3200 | Owner provide light fixture selections for podium level | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| ASI36 | ASI No. 36 - MDP Electrical Revisions Rev. 16 | 0 | 0 | 08-Apr-14 A | | |
| ASI29r1 | ASI No. 29 (Revised) - Guestroom, Interior Elevation, | 0 | 0 | 09-Apr-14 A | | |
| I-3800 | Resolve  Heat Pump Electrical Overcurrent Issue | 20 | 0 | 23-Apr-14 A | 18-Jun-14 A | |
| L10-8221 | HVAC Risers Duct Insulation | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L11-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| ASI37 | ASI No. 37 - NTI DV Drawing Revisions | 0 | 0 | 28-Apr-14 A | | |
| I-2304 | RFI 233/ Framing "Go Back" work at L3 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2306 | RFI 233/ Framing "Go Back" work at L4 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2308 | RFI 233/ Framing "Go Back" work at L5 | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2706 | Framing "Go Back" work for ASIs 23, 29 - L5 | 1 | 0 | 29-Apr-14 A | 13-May-14 A | |

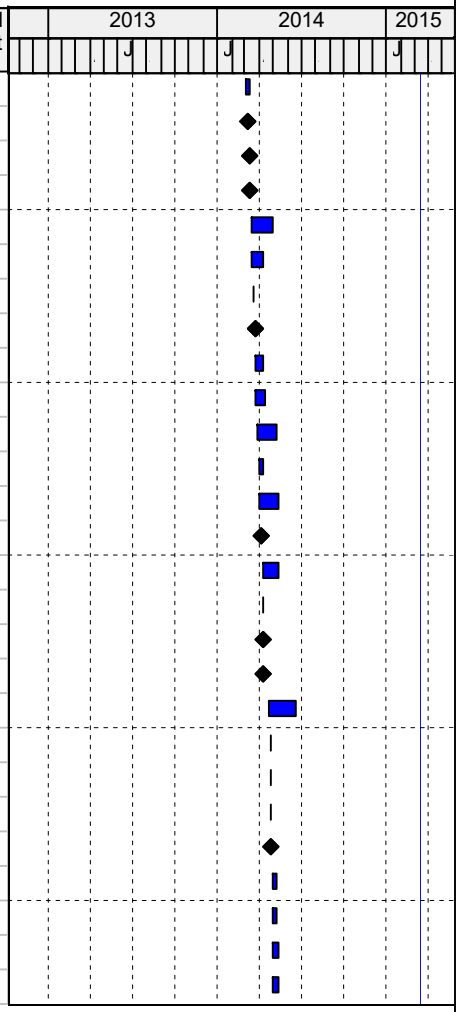



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-2708 | Framing "Go Back" work for ASIs 23, 29 - L6 | 1 | 0 | 29-Apr-14 A | 09-May-14 A | |
| I-2702 | Framing "Go Back" work for ASIs 23, 29 - L3 | 1 | 0 | 01-May-14 A | 01-May-14 A | |
| I-1706 | PSE scheduling delay | 10 | 0 | 01-May-14 A | 20-May-14 A | |
| I-3602 | Complete shop drawings & fab/deliver storefront fram | 40 | 0 | 01-May-14 A | 14-Jun-14 A | |
| L04-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| I-3904 | Ballroom Parapet Height Issue/ re-engineer parapet | 1 | 0 | 06-May-14 A | 01-Jul-14 A | |
| I-1802 | Rework framing for door hold-opens - LL4 | 1 | 0 | 07-May-14 A | 08-May-14 A | |
| L04-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-May-14 A | 12-May-14 A | |
| ASI25r1 | ASI No. 25 (Revised) - Architectural Podium Level Re | 0 | 0 | 07-May-14 A | | |
| ASI29r2 | ASI No. 29 (Revised) - Architectural Tower and Guestı | 0 | 0 | 07-May-14 A | | |
| I-1800 | Owner issue directive to proceed with door hold-open | 1 | 0 | 08-May-14 A | 08-May-14 A | |
| I-1804 | Rework framing for door hold-opens - LL3 | 1 | 0 | 08-May-14 A | 09-May-14 A | |
| I-2312 | RFI 233/ Framing "Go Back" work at L7 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-2314 | RFI 233/ Framing "Go Back" work at L8 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-3902 | Install Ballroom parapet extension | 5 | 0 | 08-May-14 A | 13-May-14 A | |
| I-1806 | Rework framing for door hold-opens - LL2 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-1808 | Rework framing for door hold-opens - LL1 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-2310 | RFI 233/ Framing "Go Back" work at L6 | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| I-2710 | Framing "Go Back" work for ASIs 23, 29 - L7 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| L05-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L06-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L05-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| LL2E-8110 | LL2 - Electrical, Fire pumps/equipment final connectic | 5 | 0 | 12-May-14 A | 30-Oct-14 A | |
| I-2316 | RFI 233/ Install dampers | 1 | 0 | 12-May-14 A | 15-May-14 A | |
| PH-8704 | PH - Install Machine Support Steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| PH-8710 | Install elevator rail support steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |

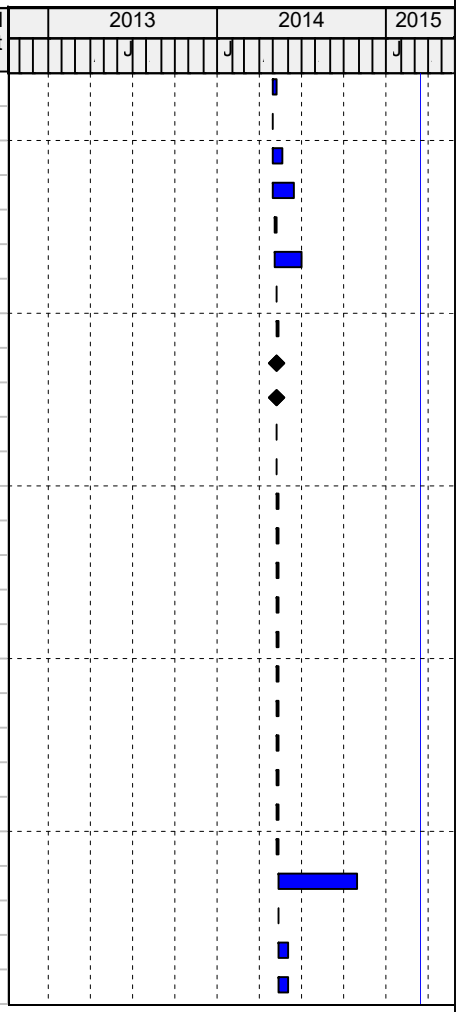


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L03-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 13-May-14 A | 14-May-14 A | |
| I-2318 | RFI 233/ Install dampers | 1 | 0 | 15-May-14 A | 19-May-14 A | |
| I-4002 | East Stitched - Install framing and windows | 9 | 0 | 19-May-14 A | 09-Jun-14 A | |
| I-2320 | RFI 233/ Install dampers | 1 | 0 | 20-May-14 A | 26-May-14 A | |
| L10-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L11-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L12-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| RF-4038 | AR - Concrete pads and curbs | 5 | 0 | 21-May-14 A | 04-Jun-14 A | |
| ASI27cap | ASI No. 27 - City Approved ASI No. 27 (Plumbing) | 0 | 0 | 21-May-14 A | | |
| ASI38 | ASI No. 38 - MDP's Bar & Concierge Plumbing Revisi | 0 | 0 | 22-May-14 A | | |
| L10-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L11-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L12-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L14-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L15-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 27-May-14 A | |
| L11-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 07-Jun-14 A | |
| L12-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 27-May-14 A | 06-Jun-14 A | |
| I-2322 | New Activity | 1 | 0 | 27-May-14 A | 28-May-14 A | |
| I-3002 | ASI 38/ City of Bellevue approve bar design changes | 5 | 0 | 28-May-14 A | 12-Dec-14 A | |
| I-4502 | Release metal panels for fabrication | 0 | 0 | 28-May-14 A | | |
| I-4504 | Metal panel fabrication (1st delivery) | 1 | 0 | 29-May-14 A | 08-Jul-14 A | |
| I-2324 | RFI 233/ Install dampers | 1 | 0 | 29-May-14 A | 08-Jun-14 A | |
| L16-8221 | HVAC Risers Duct Insulation | 1 | 0 | 30-May-14 A | 30-May-14 A | |

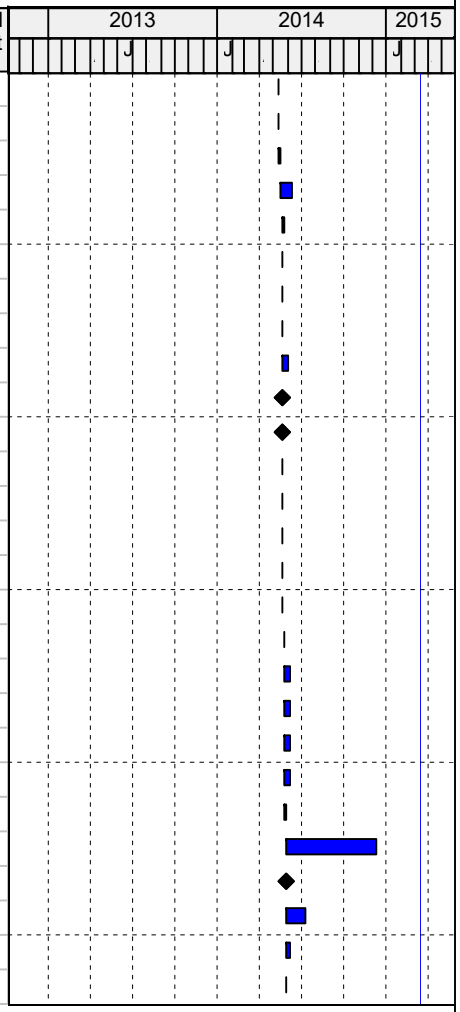



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-8712 | PH - Complete Framing and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| PH-8714 | Stage PH/L18 roofing materials | 2 | 0 | 30-May-14 A | 30-May-14 A | |
| L08-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L08-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 02-Jun-14 A | 20-Jun-14 A | |
| PH-8704I | Correct support steel embeds | 2 | 0 | 02-Jun-14 A | 11-Jun-14 A | |
| L14-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 03-Jun-14 A | 04-Jun-14 A | |
| L17-8221 | HVAC Risers Duct Insulation | 1 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| PC-4010 | PC - Fireproof Entry Roof Steel | 5 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| I-4100 | Owner resolve trap primers issue (RFI 560) | 5 | 0 | 03-Jun-14 A | 20-Jun-14 A | |
| RF-6028 | Tower Roof - Structural Steel | 5 | 0 | 04-Jun-14 A | 17-Jun-14 A | |
| L14-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L1B-6005 | Head of Wall Fire Caulk at CMU (including East Servic | 2 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| ASI36r1 | ASI No. 36 (Revised) - MDP's Revision to E002 | 0 | 0 | 05-Jun-14 A | | |
| L14-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L15-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L16-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| ASI39 | ASI No. 39 - MDP's Electrical Revisions Rev. 17 | 0 | 0 | 09-Jun-14 A | | |
| I-2326 | RFI 233/ Install dampers | 1 | 0 | 09-Jun-14 A | 09-Jun-14 A | |
| I-2328 | RFI 233/ Install dampers | 1 | 0 | 09-Jun-14 A | 09-Jun-14 A | |
| I-2330 | RFI 233/ Install dampers | 1 | 0 | 10-Jun-14 A | 10-Jun-14 A | |
| L09-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 11-Jun-14 A | 12-Jun-14 A | |
| ASI25r2 | ASI No. 25 (Revised) - JBA's Interior Elevation Revisic | 0 | 0 | 11-Jun-14 A | | |
| ASI29r3 | ASI No. 29 (Revised) - JBA's Interior Elevation Revs a | 0 | 0 | 11-Jun-14 A | | |

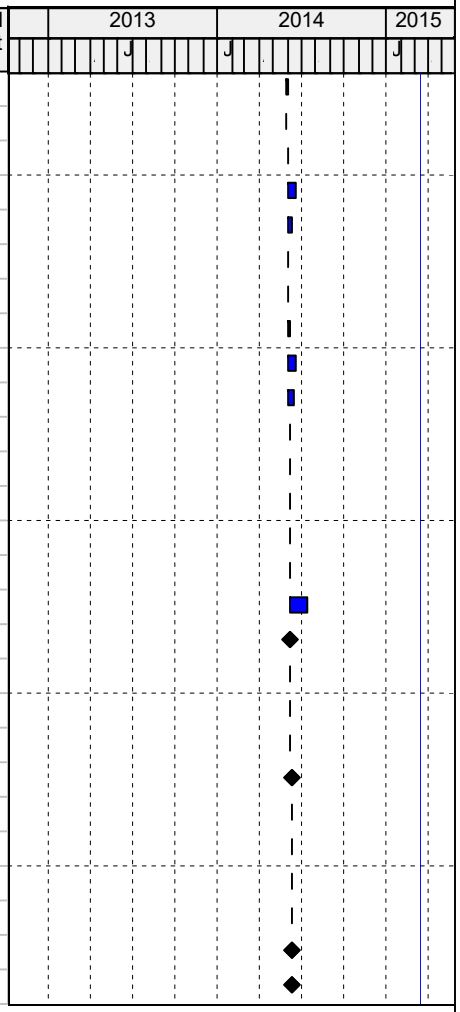


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ASI35r1 | ASI No. 35 (Revised) - JBA's Interior Design Revisions | 0 | 0 | 11-Jun-14 A | | |
| I-2332 | RFI 233/ Install dampers | 1 | 0 | 11-Jun-14 A | 12-Jun-14 A | |
| I-5018 | RFI 566 - Street Overlay Pavement Marking Reqs | 1 | 0 | 11-Jun-14 A | 01-Jul-14 A | |
| I-2970 | RFI 567 Grease Duct Conflict with Mens Restroom (P | 1 | 0 | 12-Jun-14 A | 01-Aug-14 A | |
| I-2336 | RFI 233/ Install dampers | 1 | 0 | 13-Jun-14 A | 16-Jun-14 A | |
| I-2334 | RFI 233/ Install dampers | 1 | 0 | 17-Jun-14 A | 18-Jun-14 A | |
| I-3702 | Complete wall framing at Stair/Elevator 5 (LL4) | 2 | 0 | 18-Jun-14 A | 20-Jun-14 A | |
| I-3720 | Fireproof added steel between Stair 1 and Elevator 5 | 5 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| I-3722 | Complete GWB between Stair 1 and Elevator 5 shaft | 10 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| ASI40 | ASI No. 40 - MDP's Electrical Revisions Rev. 18 | 0 | 0 | 18-Jun-14 A | | |
| LL1-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 22-Jul-14 A | |
| TC-5912 | Tower Crane pour-backs (LL4 to L3) | 4 | 0 | 19-Jun-14 A | 26-Jun-14 A | |
| LL1-Z2-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| I-2338 | RFI 233/ Install dampers | 1 | 0 | 19-Jun-14 A | 23-Jun-14 A | |
| LL4-6005 | LL4 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| LL3-6005 | LL3 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| L03-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 21-Jun-14 A | 21-Jun-14 A | |
| L06-6040 | Test Heat Pumps - L3, L4, L5 and L6 | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L03-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| L17-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL2-6005 | LL2 - Seismic Head Of Wall Fire Caulk at CMU | 5 | 0 | 24-Jun-14 A | 18-Jul-14 A | |
| I-3704 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL1-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z2-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z3-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 04-Aug-14 A | |
| L1L-6005 | Head of Wall Fire Caulk at CMU (including back of ho | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1K-6005 | Head of Wall Fire Caulk at CMU & Inspection | 2 | 0 | 24-Jun-14 A | 08-Aug-14 A | |

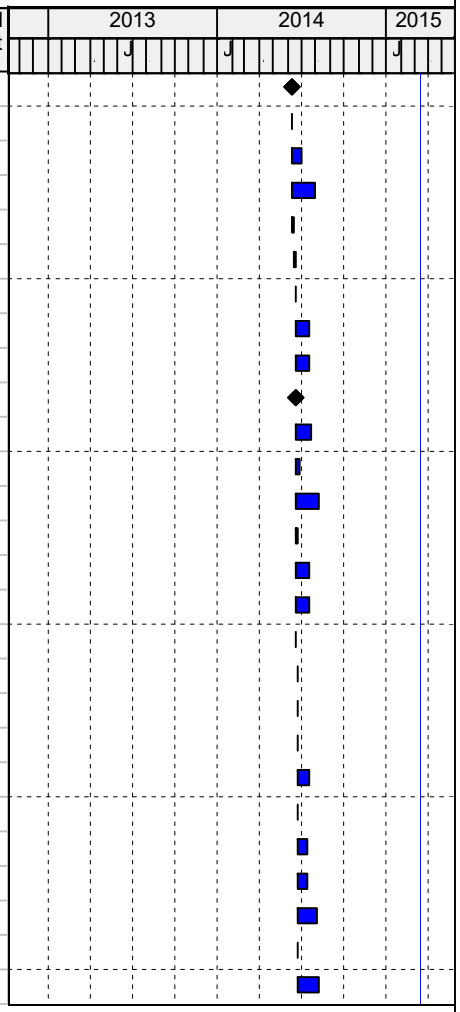



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L04-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| I-2340 | RFI 233/ Install dampers | 1 | 0 | 24-Jun-14 A | 26-Jun-14 A | |
| L17-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| I-3710 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| I-3712 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| L1K-6018a | Install Kitchen hoods and grease ducts (OFCI) | 10 | 0 | 25-Jun-14 A | 07-Oct-14 A | |
| L03-8604 | L3 Pool - Plumbing R/I | 5 | 0 | 25-Jun-14 A | 10-Nov-14 A | |
| ASI41 | ASI No. 41 - Kay Lang's Interior Design CD Set | 0 | 0 | 25-Jun-14 A | | |
| L04-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 26-Jun-14 A | 03-Jul-14 A | |
| L09-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 26-Jun-14 A | 26-Jun-14 A | |
| I-3706 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 26-Jun-14 A | 10-Jul-14 A | |
| L03-8600 | L3 Pool - Framing & HM frames | 5 | 0 | 26-Jun-14 A | 20-Nov-14 A | |
| L05-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L08-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L04-7018 | Electrical Rough-In | 1 | 0 | 27-Jun-14 A | 22-Jul-14 A | |
| L04-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 27-Jun-14 A | 23-Jul-14 A | |
| I-2342 | RFI 233/ Install dampers | 1 | 0 | 27-Jun-14 A | 28-Jun-14 A | |
| L03-7020 | HVAC Rough-In | 1 | 0 | 29-Jun-14 A | 15-Jul-14 A | |
| L1RR-8100 | Insulation [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8100 | Insulation [DELETED - included in Ballroom activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8100 | Insulation [DELETED - included in Meeting Rooms ac | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8102 | GWB Hang [DELETED - included in Meeting Rooms a | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8215 | GWB Tape [DELETED - included in Meeting Rooms a | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8104 | Prime Paint [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |

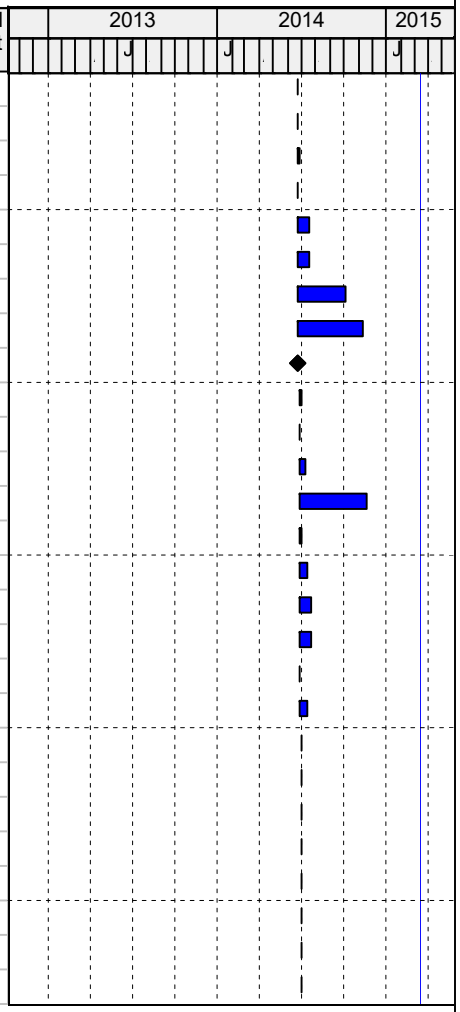


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z6-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8102 | GWB Hang [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8215 | GWB Tape [DELETED - included in Ballroom activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8104 | Prime Paint [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8102 | GWB Hang [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8215 | GWB Tape [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8104 | Prime Paint [DELETED - included in Kitchen activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L03-7018 | Electrical Rough-In | 1 | 0 | 01-Jul-14 A | 14-Jul-14 A | |
| L03-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Jul-14 A | 15-Jul-14 A | |
| I-5020 | RFI 583 - Tree Grate Location | 1 | 0 | 01-Jul-14 A | 23-Jul-14 A | |
| I-5022 | RFI 585 - Porte Cochere Concrete Bench & Planters | 1 | 0 | 01-Jul-14 A | 09-Jul-14 A | |
| I-5024 | RFI 586 - Bench Support at Porte Cochere (related to | 1 | 0 | 01-Jul-14 A | 09-Jul-14 A | |
| L10-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7102 | Install Vertical Heat Pump | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L03-7116 | Frame Walls | 1 | 0 | 02-Jul-14 A | 14-Jul-14 A | |
| L03-7118 | Install HM Door Frame | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L04-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L05-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L07-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L08-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |

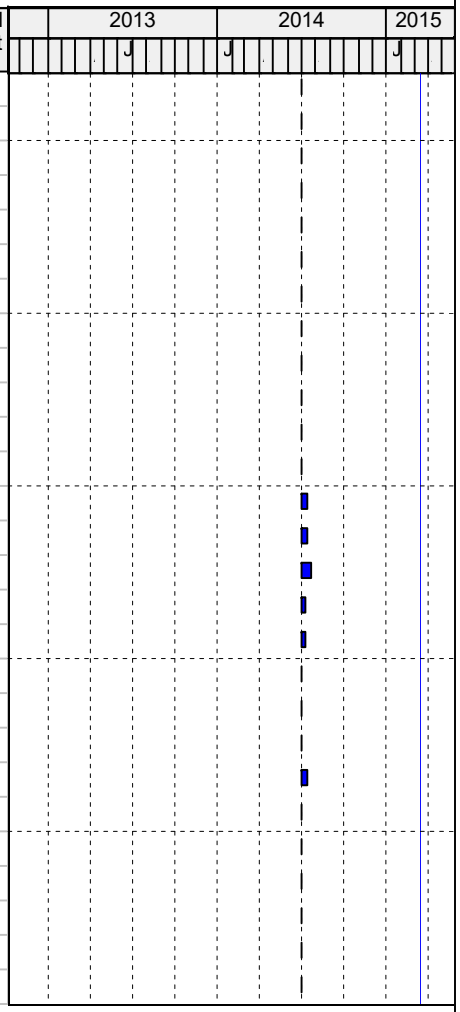



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L10-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L12-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| I-3906 | Ballroom Parapet Height Issue/ frame parapet | 1 | 0 | 02-Jul-14 A | 21-Jul-14 A | |
| L06-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| I-3708 | Complete wall framing at Stair/Elevator 5 (LL3) | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L11-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 03-Jul-14 A | 07-Jul-14 A | |
| L04-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L05-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L06-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L07-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L08-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L17-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L10-6040 | Test Heat Pumps - L7, L8, L9 and L10 | 3 | 0 | 07-Jul-14 A | 09-Jul-14 A | |
| L10-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L03-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |

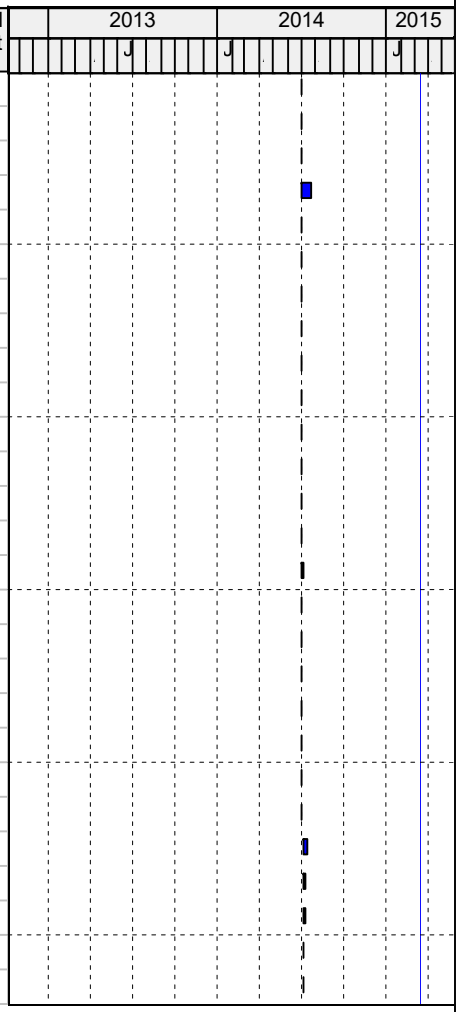



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L04-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L05-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L06-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L07-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L08-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L09-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L10-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L12-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L14-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L11-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Jul-14 A | 29-Jul-14 A | |
| L03-8602 | L3 Pool - Fire Sprinkler R/I | 5 | 0 | 08-Jul-14 A | 22-Jul-14 A | |
| L03-7016 | Install HM door frame | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L11-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L16-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 09-Jul-14 A | |
| L04-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |

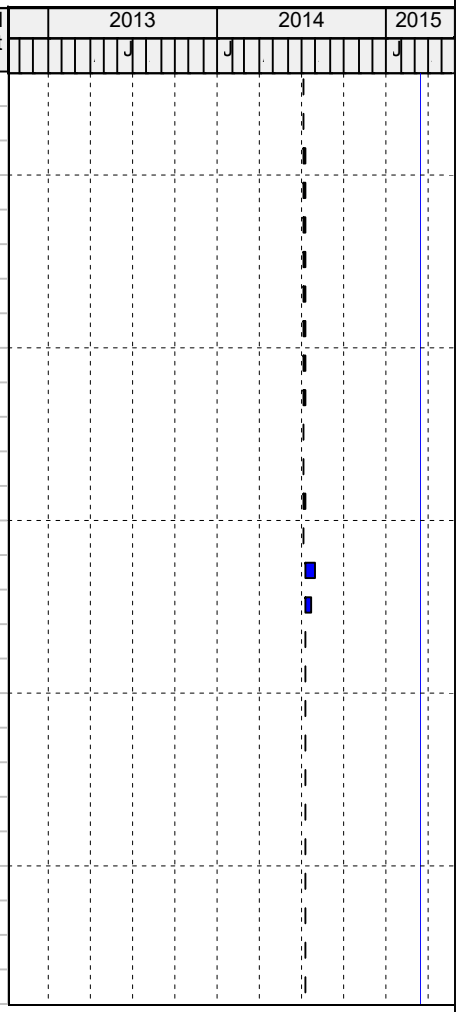



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L12-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| MP-FAB1 | Fabricate and Deliver Bronze Gold Horizontal Panels | 30 | 0 | 09-Jul-14 A | 15-Jul-14 A | |
| L04-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L05-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L06-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L16-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| MP-FAB2 | Fabricate and Deliver Silver Vertical Panels | 45 | 0 | 10-Jul-14 A | 25-Aug-14 A | |

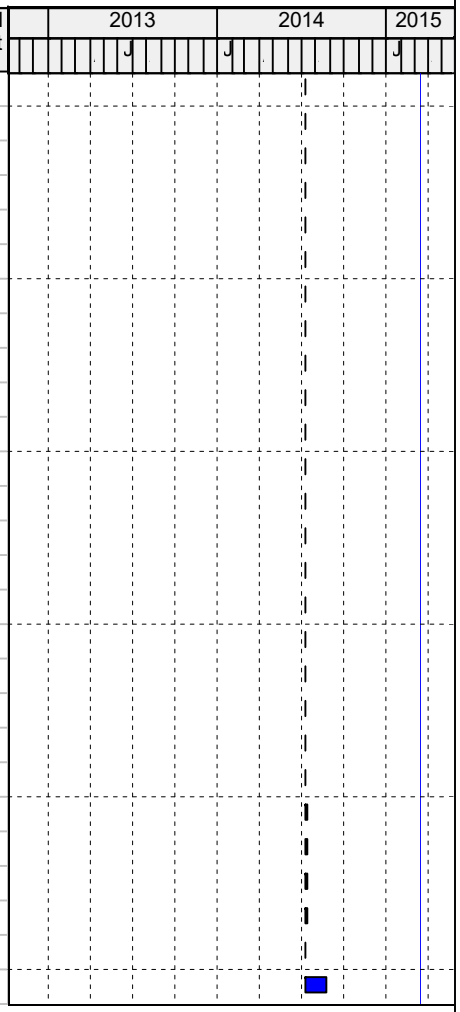



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ASI27capt | ASI No. 27 - City Approved ASI No. 27 (Tower Plumbi | 0 | 0 | 10-Jul-14 A | | |
| ASI27cam | ASI No. 27 - City Approved ASI No. 27 (Mechanical) | 0 | 0 | 10-Jul-14 A | | |
| ASI36ca | ASI No. 36 - MDP Electrical Revisions Rev. 16 (City Ap | 0 | 0 | 10-Jul-14 A | | |
| ASI38ca | ASI No. 38 - MDP's Bar & Concierge Plumbing Revisi | 0 | 0 | 10-Jul-14 A | | |
| I-5026 | RFI 611 - Landscaping at Porte Cochere Planters | 1 | 0 | 10-Jul-14 A | 18-Jul-14 A | |
| I-3004 | ASI 38/ Issue ASI 38 | 0 | 0 | 11-Jul-14 A | | |
| I-3006 | ASI 38/ Release bar area for x-ray examination | 5 | 0 | 11-Jul-14 A | 03-Sep-14 A | |
| L07-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| LL1-Z2-6018a | Complete Mech RI at tower crane opening (LL1) | 4 | 0 | 14-Jul-14 A | 17-Jul-14 A | |
| L08-6223 | Frame Corridor Ceilings | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| SW-2006a | Complete Dry Utilities (Phase 2) | 5 | 0 | 14-Jul-14 A | 24-Jul-14 A | |
| L04-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L04-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L05-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L06-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L04-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |

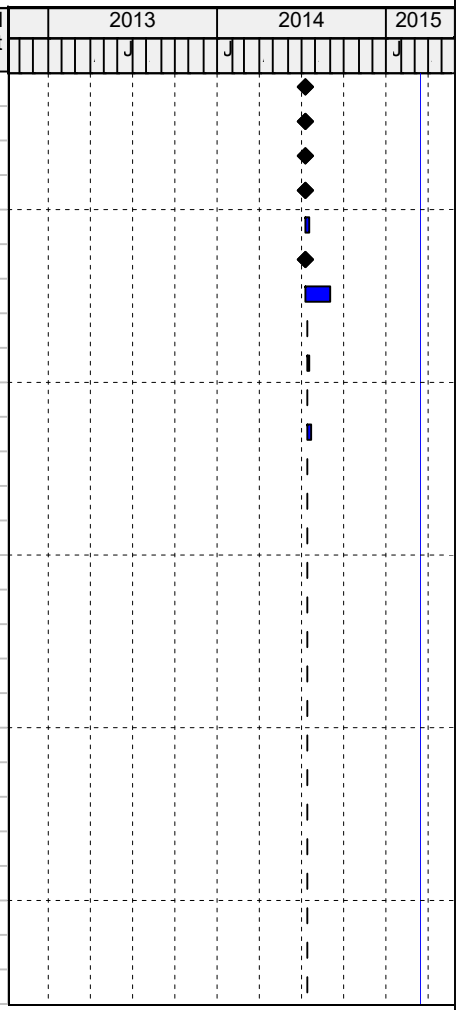



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L11-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L11-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L12-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L12-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L15-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L15-7102 | Install Vertical Heat Pump | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L1B-6026 | Install operable partition steel | 2 | 0 | 15-Jul-14 A | 08-Aug-14 A | |
| L09-6223 | Frame corridor ceilings | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L03-7120 | Electrical Rough-In | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L07-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L07-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L08-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L08-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L09-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L09-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L03-7142 | Install Laundry Chute (All Levels) | 9 | 0 | 15-Jul-14 A | 25-Jul-14 A | |
| LL2-2045 | LL2 - Electrical Room build-out | 15 | 0 | 15-Jul-14 A | 26-Sep-14 A | |
| L03-7122 | HVAC Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |

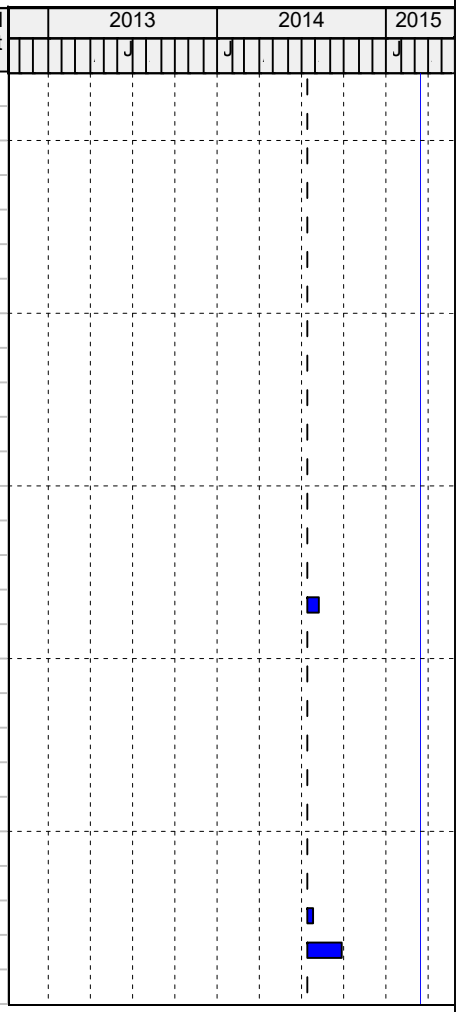



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L04-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L05-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L06-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L07-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L07-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L08-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L08-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L09-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L09-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L11-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L11-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L12-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L12-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L15-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L15-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |

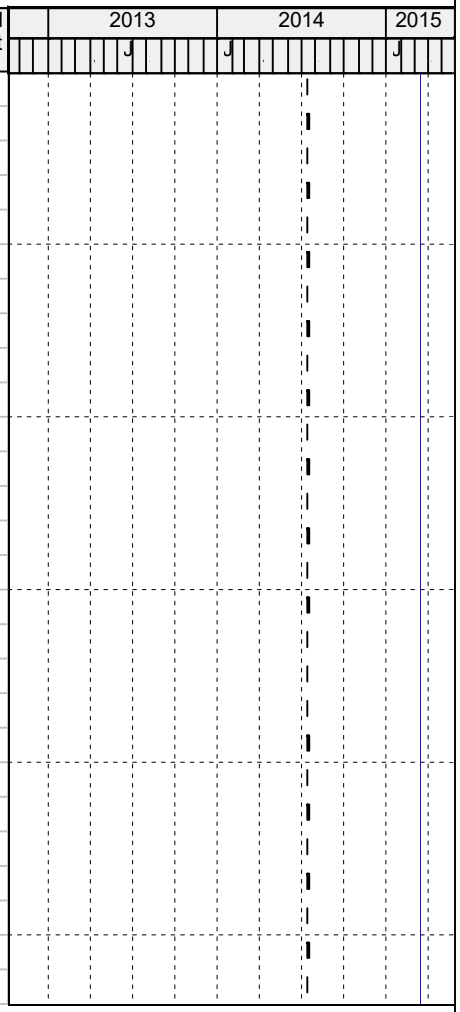



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L17-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| ASI41r1 | ASI No. 41 (Revised) - Kay Lang's Interior Design CD | 0 | 0 | 16-Jul-14 A | | |
| ASI43 | ASI No. 43 - MDP's Electrical Revisions Rev. 19 | 0 | 0 | 16-Jul-14 A | | |
| L03-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L04-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L04-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L05-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L05-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L06-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L06-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L07-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L08-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L09-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |

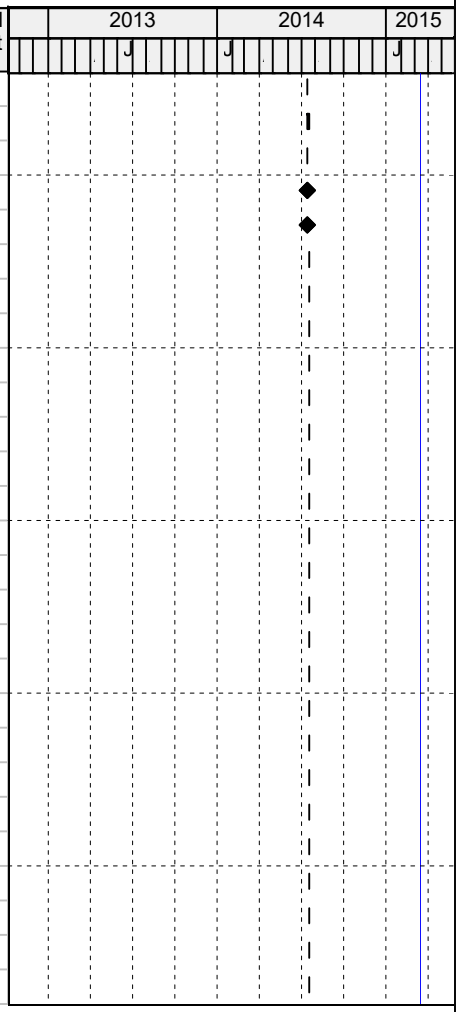



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L11-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L12-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L12-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L16-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| ASI42 | ASI No. 42 - JBA's Arch Revs to Lobby and Concierge | 0 | 0 | 17-Jul-14 A | | |
| ASI45 | ASI No. 45 - JBA's Revised Guestroom Suite Layouts | 0 | 0 | 17-Jul-14 A | | |
| L03-8608 | L3 Pool - Electrical R/I | 5 | 0 | 18-Jul-14 A | 10-Nov-14 A | |
| L03-8610 | L3 Pool - Fire Alarm / Elec Specialties R/I | 5 | 0 | 18-Jul-14 A | 10-Nov-14 A | |
| L15-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L15-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| L17-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L17-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| LL2-2052 | LL2 - Install fuel piping and exhaust duct to Generatc | 8 | 0 | 21-Jul-14 A | 15-Aug-14 A | |
| L04-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L04-7016 | Install HM door frame | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L07-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L08-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L10-7116 | Frame Walls | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L16-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 21-Jul-14 A | 22-Jul-14 A | |
| L16-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L17-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| ASI41r2 | ASI No. 41 (Revised) - Kay Lang's Interior Design Spe | 0 | 0 | 22-Jul-14 A | | |
| ASI44 | ASI No. 44 - MDP's Mechanical Revisions Rev. 17 | 0 | 0 | 24-Jul-14 A | | |
| MPT-1002 | Tower - Install Elevation 35 (east elevation-south half) | 8 | 0 | 25-Jul-14 A | 04-Aug-14 A | |
| L16-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 25-Jul-14 A | 25-Jul-14 A | |

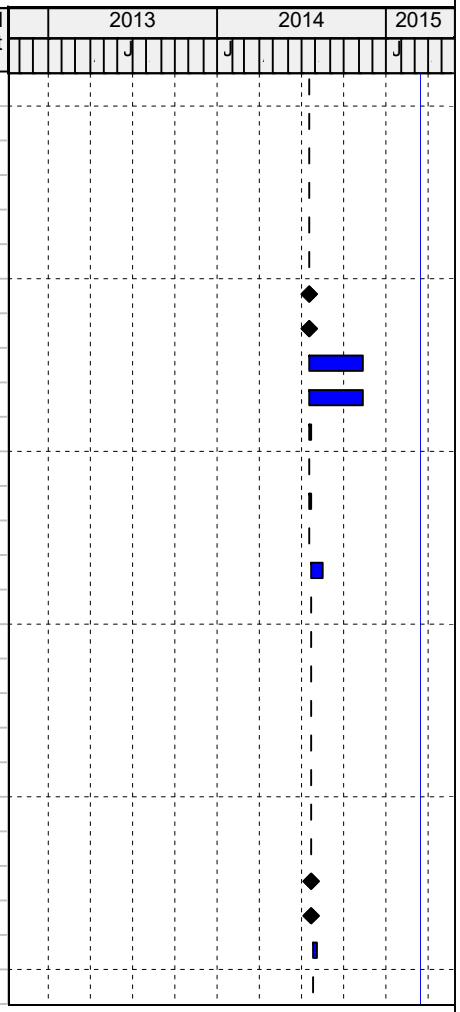


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L14-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L15-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L16-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L10-6223 | Frame Corridor Ceilings | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L11-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L15-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L15-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L11-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L14-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L16-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| I-1304 | Prep Kitchen - Additional framing (ASI 30) | 2 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-2302 | Framing "Go Back" work at LL1 for RFI 233 | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| I-2502 | Electrical rework at LL1 for ASIs 7, 9r2, 14, 27 | 4 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| L12-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L1B-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 01-Aug-14 A | 15-Aug-14 A | |
| MPL4-1000 | Upper L4 Ballroom - Install Elevations 1, 2 & 3 (south | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1000 | Tower - Install Elevations 26-27 (west elevation) [DEL | 13 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPP-1002 | Podium - Install Elevations 1 & 2 (west elevation, sou | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPP-1008 | Podium - Install Elevations 7 & 8 (north & east elevati | 9 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1002 | Upper L4 Ballroom - Install Elevation 10 (west elevatic | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |

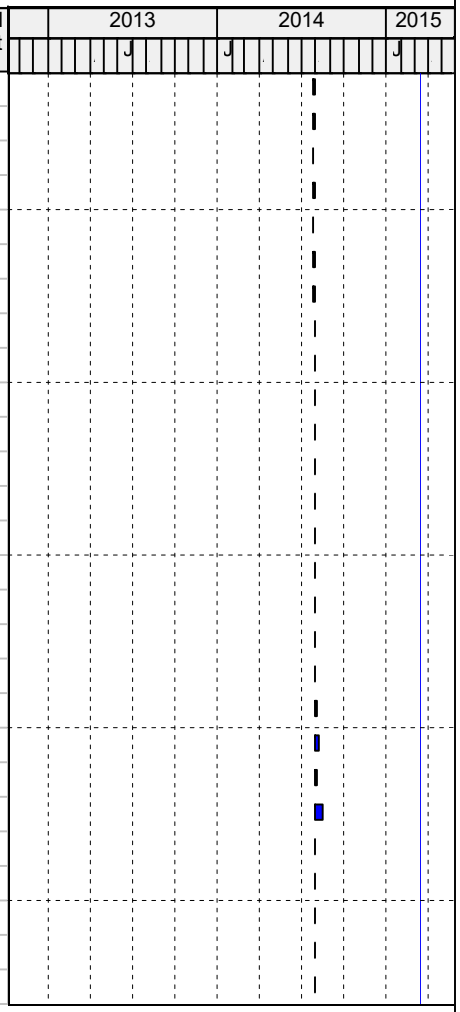



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPL4-1004 | Upper L4 Ballroom - Install Elevation 9 (north elevatio | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1006 | Tower - Install Elevation 40 (east return-east end) [DE | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1010 | Tower - Install Elevations 51 (north elevation) [DELET | 8 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-4004 | East Stitched - Install metal panels [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L11-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L11-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L15-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L14-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L17-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| MPT-1010b | Tower - Install Elevation 45 [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| ASI46 | ASI No. 46 - Concept Services Revised Kitchen Drawi | 0 | 0 | 01-Aug-14 A | | |
| L16-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 04-Aug-14 A | 05-Aug-14 A | |
| L11-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Aug-14 A | 08-Aug-14 A | |
| L04-7020 | HVAC Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |

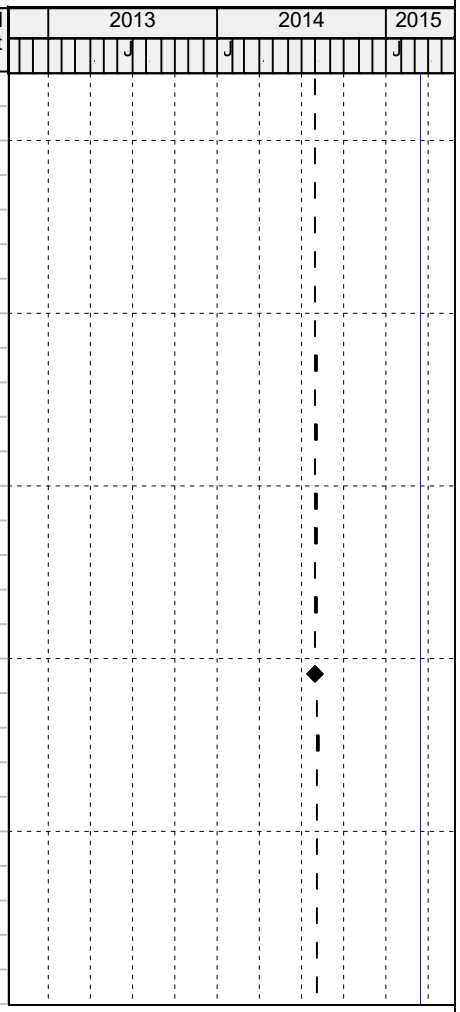



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L14-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L15-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 05-Aug-14 A | 07-Aug-14 A | |
| L05-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L06-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L07-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L08-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L09-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L10-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7018 | Electrical Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L14-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 05-Aug-14 A | 06-Aug-14 A | |
| L14-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| I-4104 | Install added trap primers - LL1 | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L06-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L07-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L08-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L09-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L10-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7020 | HVAC Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |

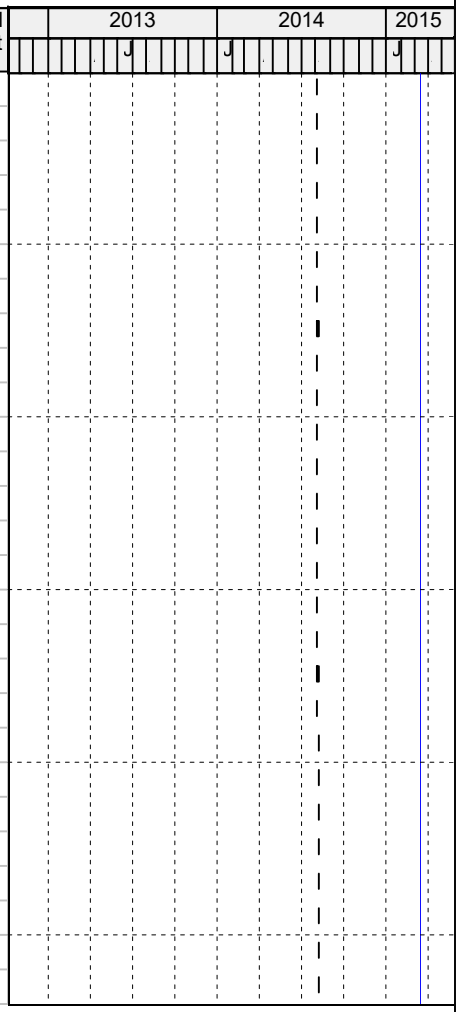



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L16-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| EL-1220 | Elevator fronts delivered | 0 | 0 | 07-Aug-14 A | | |
| L12-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L12-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-6223 | Frame Corridor Ceilings | 4 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L11-7016 | Install HM door frame | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L12-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L15-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L15-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L16-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L16-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L17-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L17-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| ASI48 | ASI No. 48 - MDP Revisions to Electrical & Plumbing | 0 | 0 | 08-Aug-14 A | | |
| L14-6040 | Test Heat Pumps - L11, L12 and L14 | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| PH-6026 | PH - Insulation/Vapor Barrier/GWB at Exterior Walls | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| L11-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |

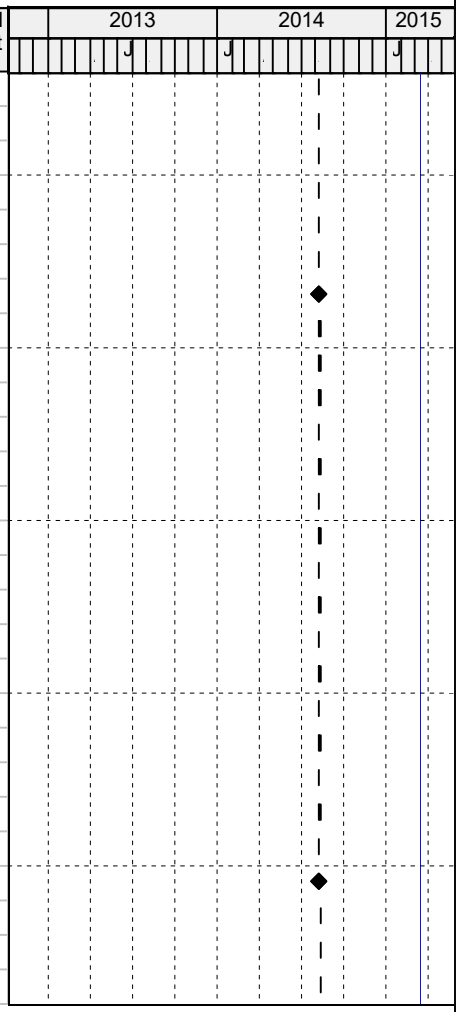



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-7026 | Inspections for GWB Cover | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 13-Aug-14 A | 13-Aug-14 A | |
| L15-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 14-Aug-14 A | 15-Aug-14 A | |
| LL2E-8108 | LL2 - Set fire pumps and equipment | 5 | 0 | 14-Aug-14 A | 29-Sep-14 A | |
| L10-7028 | GWB Hang/Tape/Finish | 5 | 0 | 14-Aug-14 A | 05-Dec-14 A | |
| L12-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L12-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L16-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L1BOH2-6008 | Int Wall Framing & Inspection | 5 | 0 | 14-Aug-14 A | 20-Aug-14 A | |
| I-4106 | Install added trap primers - L1 | 1 | 0 | 15-Aug-14 A | 15-Aug-14 A | |
| L14-6223 | Frame Corridor Ceilings | 4 | 0 | 15-Aug-14 A | 16-Aug-14 A | |
| L03-8136 | Install Counter Subtops | 3 | 0 | 15-Aug-14 A | 18-Aug-14 A | |
| LL2-2054 | LL2 - GWB, Hang 1st Layer at Laundry Room | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| LL2E-8112 | LL2 - Form/Pour Fire Pump Pads/Curbs | 2 | 0 | 16-Aug-14 A | 18-Aug-14 A | |
| LL1-6014Ia | L1 bar redesign - rework plumbing at ceilings | 10 | 0 | 18-Aug-14 A | 05-Jan-15 A | |
| L15-6223 | Frame Corridor Ceilings | 4 | 0 | 18-Aug-14 A | 21-Aug-14 A | |

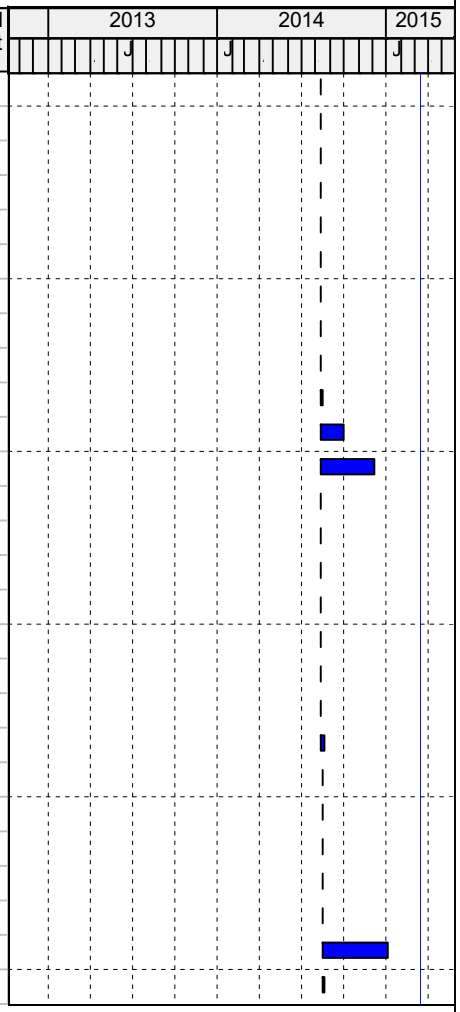



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Aug-14 A | 18-Aug-14 A | |
| L04-8136 | Install Counter Subtops | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-6014Ic | L1 bar redesign - rework electrical at ceilings | 10 | 0 | 18-Aug-14 A | 05-Jan-15 A | |
| LL2E-8114 | LL2 - Set Tube Steel at Door | 1 | 0 | 19-Aug-14 A | 19-Aug-14 A | |
| L17-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 20-Aug-14 A | 21-Aug-14 A | |
| L17-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 20-Aug-14 A | 20-Aug-14 A | |
| L05-8136 | Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 26-Aug-14 A | |
| L06-8136 | Bathrooms - Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 13-Oct-14 A | |
| L16-6223 | Frame Corridor Ceilings | 4 | 0 | 21-Aug-14 A | 29-Aug-14 A | |
| L17-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 21-Aug-14 A | 22-Aug-14 A | |
| L17-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 21-Aug-14 A | 21-Aug-14 A | |
| L1BOH2-6016 | Electrical RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6018 | HVAC RI | 4 | 0 | 21-Aug-14 A | 17-Oct-14 A | |
| L15-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7020 | HVAC Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7022 | Fire Sprinkler Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| LL2E-8116 | LL2 - Set Door Jamb | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| ASI49 | ASI No. 49 - SCA Transformer Vault Alcove Connectic | 0 | 0 | 22-Aug-14 A | | |
| L03-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L04-7028 | GWB Hang/Tape/Finish | 5 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L05-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L05-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L06-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |

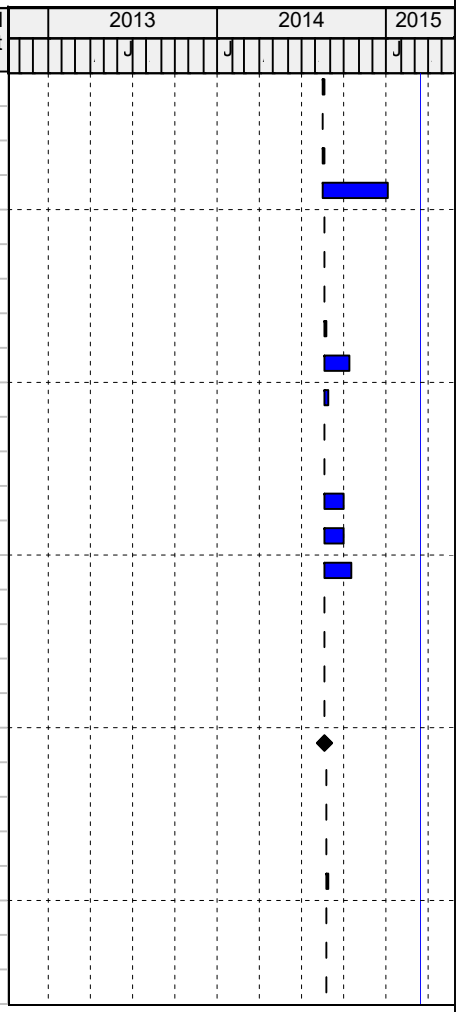



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L03-8123 | Bathroom "Barn Doors" On Site | 0 | 0 | 25-Aug-14 A | | |
| LL3-6026 | LL3 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL2-6026 | LL2 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL1-Z3-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L1BOH2-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |

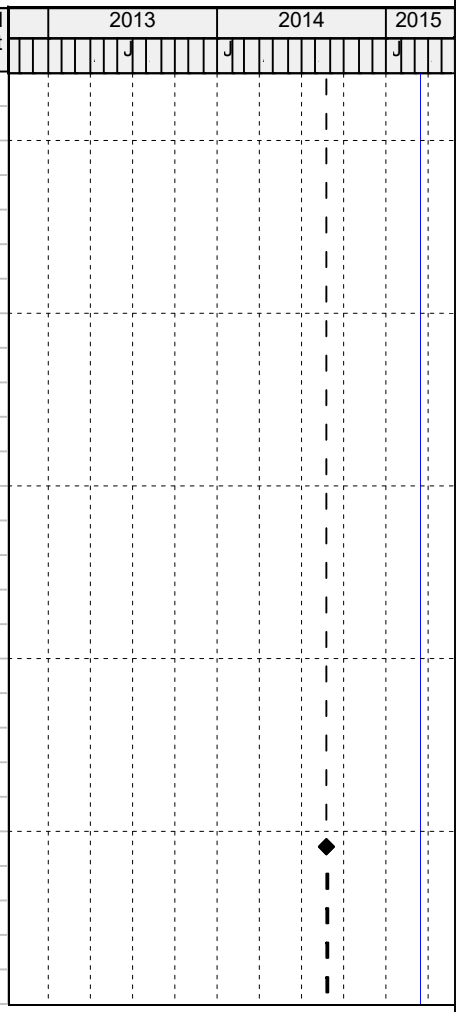



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-6026 | L2 - Set Elevator Fronts (Cars 1-4 | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L03-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L04-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L05-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L06-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L07-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L08-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L09-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L10-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L11-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L12-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L14-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L15-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L16-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L17-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| MPT-1008 | Tower - Install E/W Wing, N. Side West Half (Elev 50,: | 7 | 0 | 26-Aug-14 A | 03-Oct-14 A | |
| L06-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L07-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L08-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L05-7026 | Inspections for GWB Cover | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L05-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L11-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 08-Dec-14 A | |
| L12-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L14-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L03-8105a | Painting - Split Door Jambs | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L09-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L10-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |

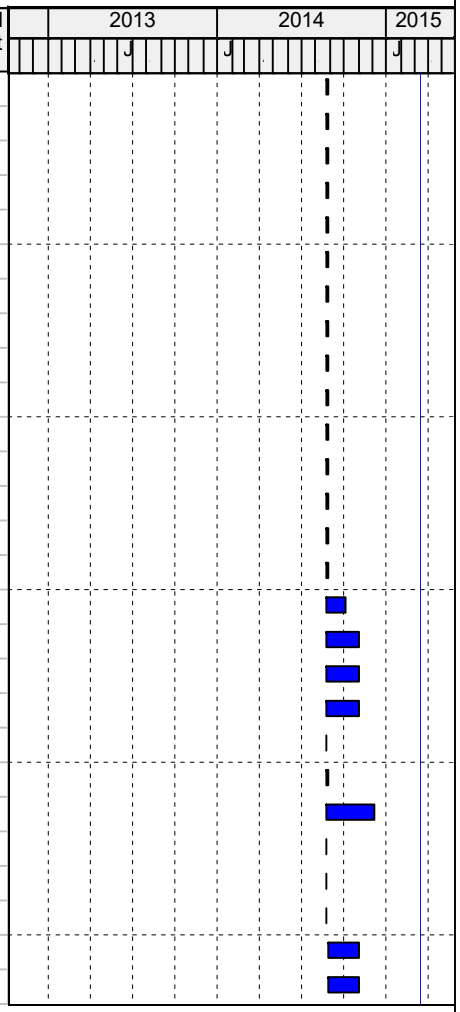



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L12-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L14-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L15-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L16-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L05-8201 | Install ACT Grid @ Corridors | 2 | 0 | 27-Aug-14 A | 28-Aug-14 A | |
| L16-7022 | Fire Sprinkler Rough-In | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L04-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L06-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| EP-5110a | L1 - Install Steel at Revolving Door Opening | 3 | 0 | 27-Aug-14 A | 29-Aug-14 A | |
| L05-8105a | Painting - Split Door Jambs | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| ASI50 | ASI No. 50 - Updated S1 Plumbing Fixture | 0 | 0 | 28-Aug-14 A | | |
| I-4102 | Install added trap primers - LL2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4108 | Install added trap primers - L2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4110 | Install added trap primers - L3 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4112 | Install added trap primers - Roof PH | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| L03-8124d | Flooring On Site and Acclimated | 2 | 0 | 29-Aug-14 A | 01-Sep-14 A | |
| ASI47 | ASI No. 47 - Architectural and Interior Design Revisior | 0 | 0 | 29-Aug-14 A | | |
| L02-5102 | L2 - Storefront Frames | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| L04-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L05-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L17-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L03-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L12-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L14-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L07-8136 | Install Counter Subtops | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| LL1-Z3-FCC10 | FCC - Set Jamb | 1 | 0 | 02-Sep-14 A | 03-Sep-14 A | |

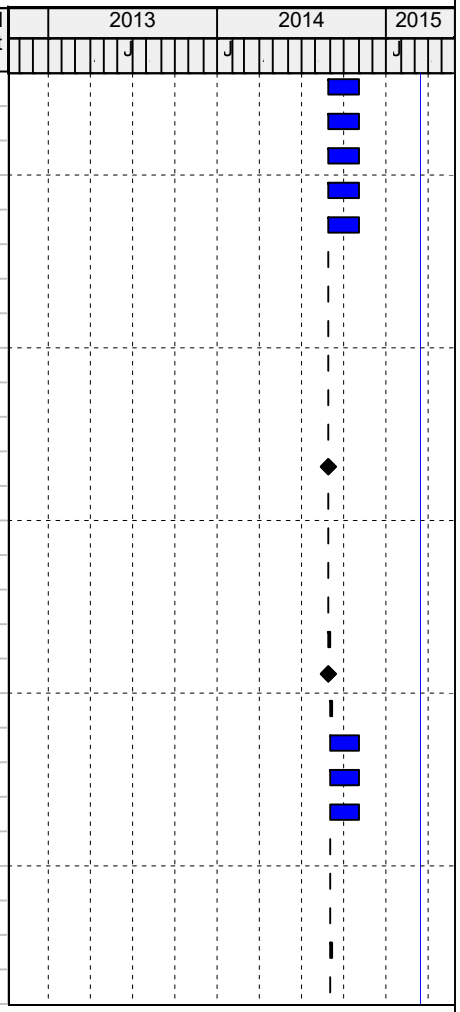



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPT-1004 | Tower - Install E/W Wing, S. Side w/o Windows (Elev | 10 | 0 | 03-Sep-14 A | 17-Oct-14 A | |
| L03-7028 | GWB Hang/Tape/Finish | 5 | 0 | 03-Sep-14 A | 02-Dec-14 A | |
| L12-7028 | GWB Hang/Tape/Finish | 5 | 0 | 03-Sep-14 A | 08-Dec-14 A | |
| L03-8126a | Doors & Hardware On Site | 0 | 0 | 03-Sep-14 A | | |
| LL1-Z3-FCC12 | FCC - Sheetrock Outside Wall | 1 | 0 | 03-Sep-14 A | 03-Sep-14 A | |
| ASI46r1 | ASI No. 46 (Revised) - Revised Kitchen Equipment M | 0 | 0 | 03-Sep-14 A | | |
| L16-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| L17-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Sep-14 A | 11-Sep-14 A | |
| L02-5104b | L2 - Install Storefront Temporary Enclosures | 1 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| LL1-Z3-FCC14 | FCC - Verify Fire Caulk OK & Inspect Room OK to 2n | 1 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| I-3008 | ASI 38/ Coordinate and perform x-ray examination | 7 | 0 | 04-Sep-14 A | 24-Sep-14 A | |
| L02-5104a | L2 - Measure/Fabricate Storefront Glazing | 15 | 0 | 05-Sep-14 A | 18-Sep-14 A | |
| LL1-Z3-FCC16 | FCC - GWB, Hang 2nd Layer | 2 | 0 | 05-Sep-14 A | 08-Sep-14 A | |
| ASI52 | ASI No. 52 - MDP Electrical Revisions Rev. 21 | 0 | 0 | 05-Sep-14 A | | |
| I-5028 | RFI 687 - Planter at Porte Cochere Grid V & 25 | 1 | 0 | 05-Sep-14 A | 10-Sep-14 A | |
| L03-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L15-7018 | Electrical Rough-In | 1 | 0 | 08-Sep-14 A | 08-Sep-14 A | |
| EL-1228 | Construct/Approve elevator lobby framing mockup (L | 3 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| LL2E-8118 | LL2 - Frame Infill, Install Densglass & Inspect at Fire I | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L06-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L08-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L15-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7018 | Electrical Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L3-5104a | L3 - Measure/Fabricate Storefront Glazing | 15 | 0 | 09-Sep-14 A | 30-Sep-14 A | |

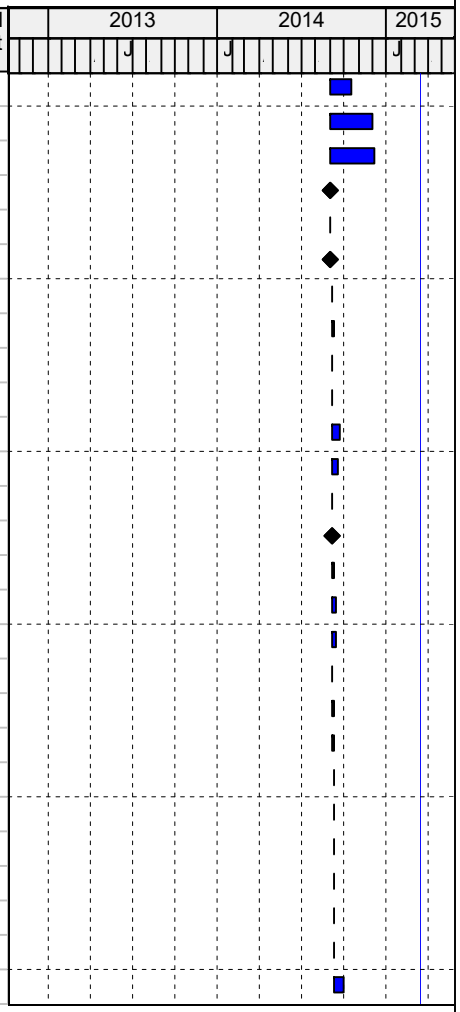



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 23-Sep-14 A | |
| L03-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L04-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L06-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| L08-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| L05-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L06-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L06-7028 | GWB Hang/Tape/Finish | 5 | 0 | 10-Sep-14 A | 02-Dec-14 A | |
| L08-7028 | GWB Hang/Tape/Finish | 5 | 0 | 10-Sep-14 A | 05-Dec-14 A | |
| L15-7026 | Inspections for GWB Cover | 1 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| LL2E-8120 | LL2 - Insulation, Vapor Barrier & Inspect at Fire Pump | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| ASI53 | ASI No. 53 - Pool Chemical Storage System | 0 | 0 | 10-Sep-14 A | | |
| L08-8395 | Framing at Elevator Lobby | 4 | 0 | 11-Sep-14 A | 17-Sep-14 A | |
| L15-7028 | GWB Hang/Tape/Finish | 5 | 0 | 11-Sep-14 A | 08-Dec-14 A | |
| L08-8136 | Install Counter Subtops | 3 | 0 | 11-Sep-14 A | 16-Sep-14 A | |
| L02-6025 | L2 - Framing Go-Back Work (left out for mechanical e | 4 | 0 | 11-Sep-14 A | 02-Oct-14 A | |
| L1-5104a | L1 - Measure/Fabricate Storefront Glazing | 15 | 0 | 12-Sep-14 A | 18-Sep-14 A | |
| L1B-8102c | Finish framing and MEP at Main Ballroom East Wall ( | 10 | 0 | 12-Sep-14 A | 02-Oct-14 A | |
| L09-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L10-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L11-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L12-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L16-7026 | Inspections for GWB Cover | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| MPT-1014 | Tower - Install E/W Wing, N. Side, E. Half (Elev 46-49 | 8 | 0 | 15-Sep-14 A | 28-Oct-14 A | |
| LL2-6032 | LL2 - Complete Framing (Including Elevator Lobby) | 4 | 0 | 15-Sep-14 A | 18-Sep-14 A | |
| L1-5104b | L1 - Install Storefront Temporary Enclosures | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |

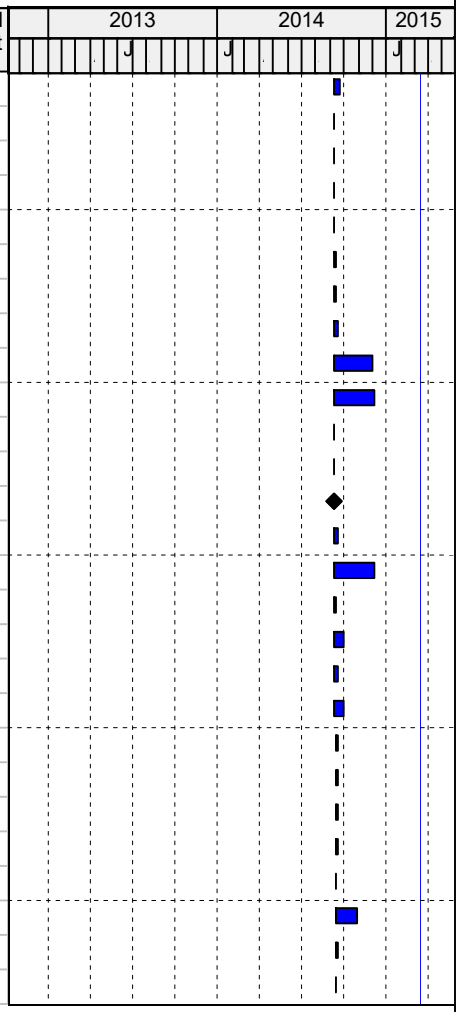


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-FCC18 | FCC - Install Temp Door | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| LL2-2058a | LL2 - GWB Hang 1st Layer | 5 | 0 | 15-Sep-14 A | 19-Sep-14 A | |
| LL2-2064 | LL2 - Generator Room - Finish Exhaust Piping | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| I-3010 | ASI 38/ Prepare proposal for MEP relocations | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| ASI51 | ASI No. 51 - Interior Design Revisions | 0 | 0 | 15-Sep-14 A | | |
| L16-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L07-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L09-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L10-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L14-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L15-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L03-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| L16-7028 | GWB Hang/Tape/Finish | 5 | 0 | 16-Sep-14 A | 08-Dec-14 A | |
| L17-7018 | Electrical Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L09-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L10-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| LL3-6028 | LL3 - Frame Elevator Lobby | 2 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| LL4-6026 | LL4 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| I-3012 | ASI 38/ Owner approve proposal for MEP relocations | 3 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| ASI50r1 | ASI No. 50 (Revised) - Updated Plumbing Fixtgure K' | 0 | 0 | 16-Sep-14 A | | |
| L11-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L12-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L14-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L15-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L04-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L17-7026 | Inspections for GWB Cover | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |

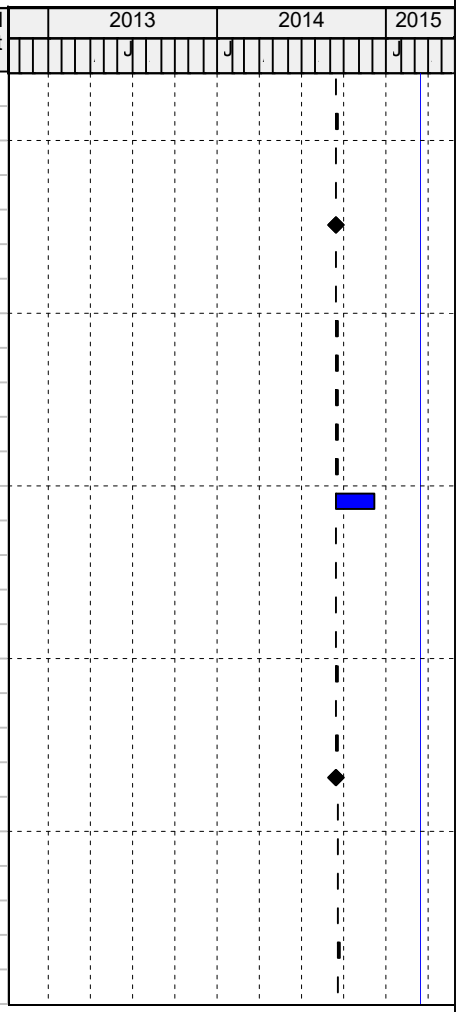



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7116 | Frame Walls | 4 | 0 | 17-Sep-14 A | 29-Sep-14 A | |
| LL2-2066 | LL2 - Generator Room - Finish Fuel Piping | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L16-8395 | Framing at Elevator Lobby | 4 | 0 | 18-Sep-14 A | 26-Sep-14 A | |
| L02-5104 | L2 - Storefront Glazing | 2 | 0 | 18-Sep-14 A | 22-Sep-14 A | |
| L17-7028 | GWB Hang/Tape/Finish | 5 | 0 | 18-Sep-14 A | 08-Dec-14 A | |
| LL4-6028 | LL4 - Frame Elevator Lobby | 2 | 0 | 18-Sep-14 A | 02-Oct-14 A | |
| MPT-1010a | Tower - Install E/W Wing, West End (Elev 52,53) | 8 | 0 | 18-Sep-14 A | 10-Oct-14 A | |
| ASI44ca | ASI No. 44 - MDP's Mechanical Revisions Rev. 17 (Ci | 0 | 0 | 18-Sep-14 A | | |
| LL2-2068 | LL2 - Generator Room - Electrical Finishes | 3 | 0 | 19-Sep-14 A | 30-Sep-14 A | |
| L07-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L09-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L04-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L05-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L03-8140 | Countertops On Site | 0 | 0 | 22-Sep-14 A | | |
| L03-8129a | Shower Doors On Site | 0 | 0 | 22-Sep-14 A | | |
| LL1-Z3-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L1BOH2-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2-2048a | LL2 - Move in Laundry Room Ironer | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2E-8122 | LL2 - Hang GWB at Fire Pump Room | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-FCC20 | FCC - Rough-In and Install Panels | 25 | 0 | 22-Sep-14 A | 21-Nov-14 A | |
| I-3014 | Core drill for MEP relocations | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L05-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L07-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 05-Dec-14 A | |
| L09-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 05-Dec-14 A | |
| L14-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 08-Dec-14 A | |
| L04-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L05-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |

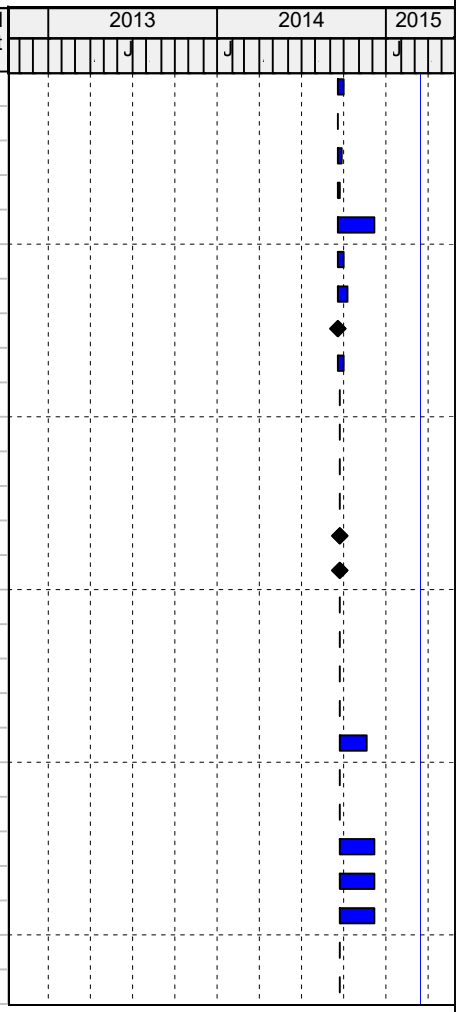



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L07-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| ASI53ca | ASI No. 53 - Pool Chemical Storage System (City Apr | 0 | 0 | 23-Sep-14 A | | |
| L04-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L06-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L04-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L05-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-7122 | HVAC Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| LL2-2058 | LL2 - Tape/Finish Laundry Room | 3 | 0 | 24-Sep-14 A | 26-Sep-14 A | |
| I-5034 | RFI 717 - Porte Cochere Paving Details | 1 | 0 | 24-Sep-14 A | 29-Oct-14 A | |
| L08-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L17-8395 | Framing at Elevator Lobby | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L05-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L06-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L07-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L08-7120 | Electrical Rough-In | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| LL2E-8124 | LL2 - Temp-In Louver Opening at Fire Pump Room | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L1-5104c | L1 - Install Storefront at Main Entry Facade | 5 | 0 | 25-Sep-14 A | 10-Oct-14 A | |
| I-5030 | RFI 715 - Additional Site Paving Per City | 1 | 0 | 25-Sep-14 A | 14-Oct-14 A | |
| L16-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |

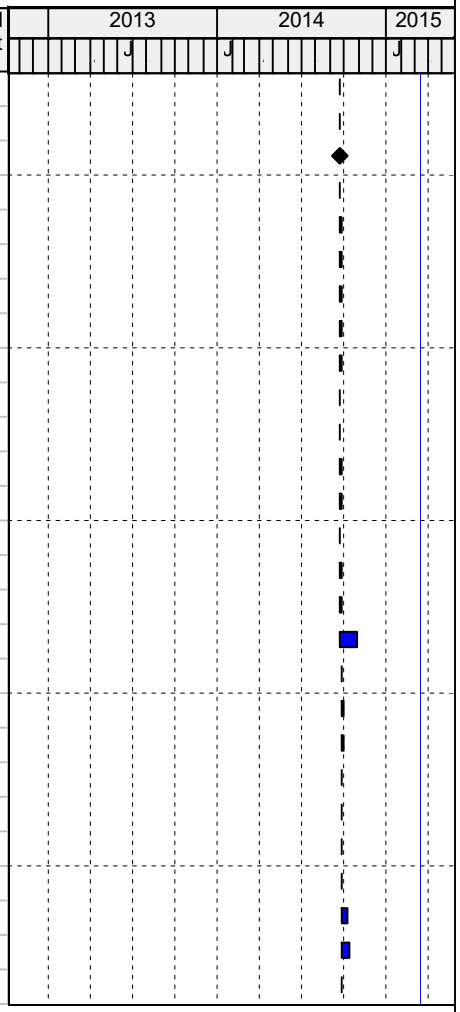



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L10-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L16-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L17-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L17-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L09-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L11-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L12-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L14-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L15-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L17-7118 | Install HM Door Frame | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| LL3-6030 | LL3 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL4-6030 | LL4 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL2-6034 | LL2 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L1BOH2-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L02-6030 | L2 - Framing at Elevator Lobby & North Half | 4 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| MPT-1022 | Tower - Caulking, west | 8 | 0 | 29-Sep-14 A | 03-Nov-14 A | |
| PH-6015 | PH - Set Boilers and Pumps | 12 | 0 | 29-Sep-14 A | 15-Oct-14 A | |
| L11-8204 | Bathrooms - Vinyl Wall Coverings | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L10-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L17-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L11-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |

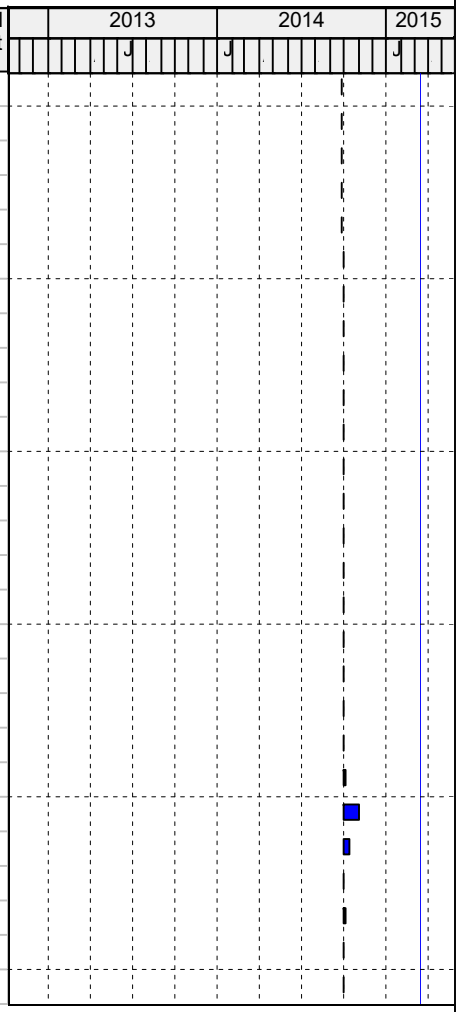



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L07-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 30-Sep-14 A | 08-Oct-14 A | |
| L11-8201 | Install ACT Grid @ Corridors | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L09-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L09-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L11-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L12-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L14-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L15-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| LL2-2072 | Generator - Complete generator and annunciator cor | 5 | 0 | 30-Sep-14 A | 21-Oct-14 A | |
| L17-6040 | Test Heat Pumps - L16 and L17 | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L17-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L14-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L03-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |

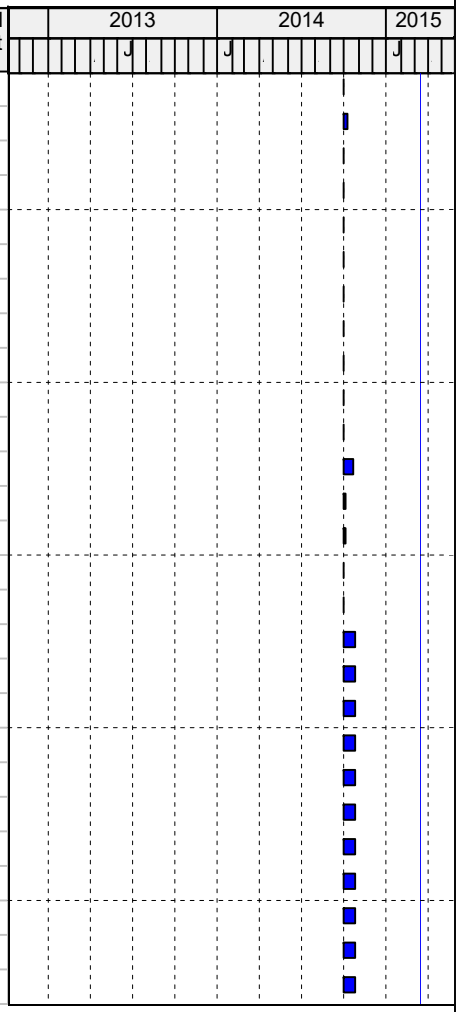



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L11-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |

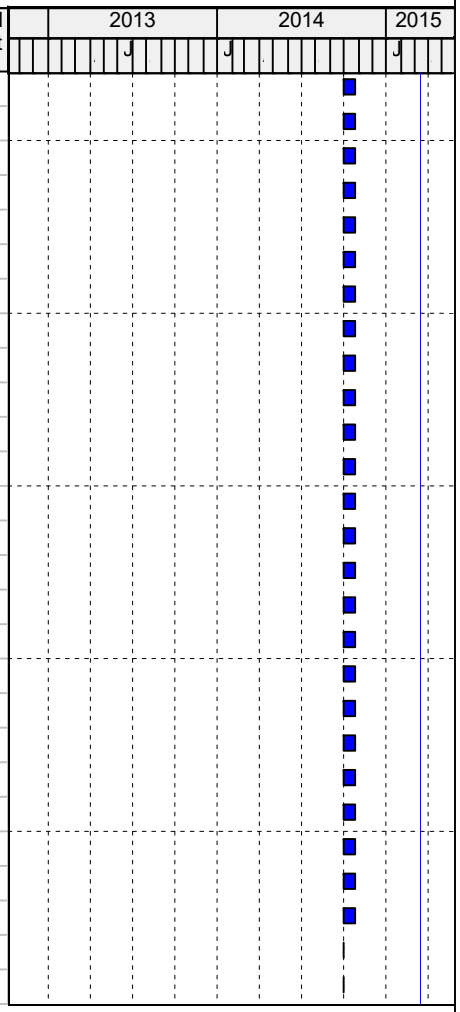



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L12-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L14-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L16-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L17-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L09-8136 | Install Counter Subtops | 3 | 0 | 01-Oct-14 A | 03-Oct-14 A | |
| L02-6032 | L2 - Electrical RI at Elevator Lobby & North Half | 5 | 0 | 01-Oct-14 A | 08-Oct-14 A | |
| SW-2306 | Prep, grind and overlay at 11th Ave, 3rd Place & 2nd | 5 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 01-Oct-14 A | 16-Dec-14 A | |
| L16-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L14-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L15-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1BOH2-8130 | Inspections For Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L02-6024a | L2 - Inspections - South Half | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L06-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| L17-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| LL2-2074 | Generator - Install fuel fill | 2 | 0 | 03-Oct-14 A | 06-Oct-14 A | |
| L07-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| MPT-1020 | Tower - Install E/W Wing, East End (Elev 41,44) | 5 | 0 | 06-Oct-14 A | 18-Oct-14 A | |
| LL1-8102a | GWB Hang/Tape (Ceilings) | 10 | 0 | 06-Oct-14 A | 18-Nov-14 A | |
| L1BOH2C-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |

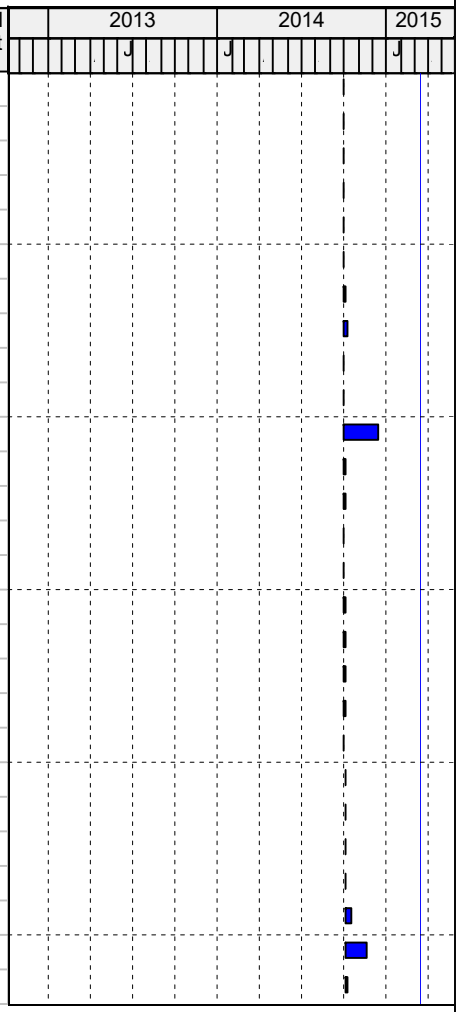


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1BOH2C-6014 | Complete Plumbing RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6016 | Complete Electrical RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6018 | Complete HVAC RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L03-8200a | New murals on site (date estimated) | 0 | 0 | 06-Oct-14 A | | |
| SW-2100 | Zone 1 - Survey curb & site lighting | 2 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 06-Oct-14 A | 06-Oct-14 A | |
| L1BOH2-8100 | Insulation | 4 | 0 | 07-Oct-14 A | 13-Oct-14 A | |
| L17-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L12-8201 | Install ACT Grid @ Corridors | 2 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| L10-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 07-Oct-14 A | 20-Oct-14 A | |
| L03-8216x | Vinyl Wall Coverings - Install Murals | 2 | 0 | 07-Oct-14 A | 29-Dec-14 A | |
| L1B-8102b | GWB Hang (Walls) & Inspection - Exterior Wall at Cor | 3 | 0 | 07-Oct-14 A | 09-Oct-14 A | |
| RF-4048 | Tower Roof - Install davit arms | 3 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| LL2-2076 | Generator - Install fuel fill mechanical piping | 4 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L12-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L09-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L03-8633 | Pool - Install waterproofing & test | 3 | 0 | 08-Oct-14 A | 17-Oct-14 A | |
| L03-8130 | Install Door Hardware | 3 | 0 | 08-Oct-14 A | 28-Oct-14 A | |
| L10-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L02-8102a | L2 - GWB Hang / Tape / Finish - South Half | 7 | 0 | 09-Oct-14 A | 27-Oct-14 A | |
| SW-2102 | Zone 1 - Vacate SE corner | 2 | 0 | 09-Oct-14 A | 11-Oct-14 A | |
| SW-2106 | Zone 1 - Sawcut and remove asphalt | 4 | 0 | 09-Oct-14 A | 14-Oct-14 A | |
| L11-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 09-Oct-14 A | |
| SW-2200 | Zone 2 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |
| SW-2300 | Zone 3 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |
| SW-2108 | Zone 1 - Install east footing drain | 4 | 0 | 10-Oct-14 A | 20-Oct-14 A | |

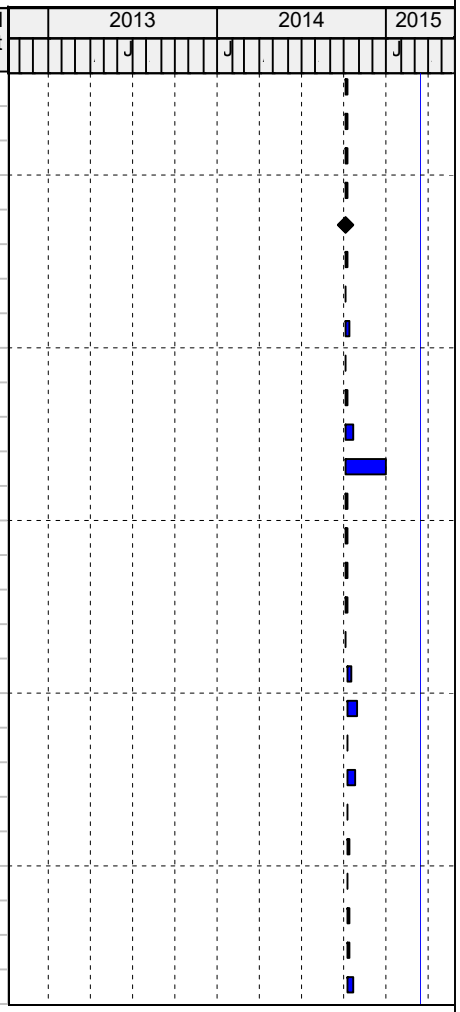


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8130 | Install Door Hardware | 3 | 0 | 10-Oct-14 A | 29-Oct-14 A | |
| ML-5962 | Man/Material Lifts - Remove Roof Lift Stop | 0 | 0 | | 11-Oct-14 A | |
| I-1102 | Additional work at new L17 guest rooms | 5 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| LL2-2046 | LL2 - Generator Room - Misc. Finishes | 3 | 0 | 13-Oct-14 A | 21-Nov-14 A | |
| RF-4008 | Tower Roof - Install corrugated metal panels | 5 | 0 | 13-Oct-14 A | 03-Nov-14 A | |
| MPT-1018b | Tower - Roof cornice frame & sheath | 6 | 0 | 13-Oct-14 A | 24-Oct-14 A | |
| L02-8100a | L2 - Insulation - South Half | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| SW-2112 | Zone 1 - Grade for curb and gutter | 3 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| SW-2202 | Zone 2 - Install site lighting | 5 | 0 | 13-Oct-14 A | 24-Nov-14 A | |
| SW-2204 | Zone 2 - Repave utility trenches | 4 | 0 | 13-Oct-14 A | 22-Oct-14 A | |
| L12-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 13-Oct-14 A | |
| I-5038 | RFI 735 - Landscape Irrigation Conflict | 1 | 0 | 13-Oct-14 A | 03-Nov-14 A | |
| SW-2302 | Zone 3 - Grade for curb and gutter | 2 | 0 | 14-Oct-14 A | 01-Dec-14 A | |
| L14-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 14-Oct-14 A | 16-Oct-14 A | |
| L05-8130 | Install Door Hardware | 3 | 0 | 14-Oct-14 A | 03-Nov-14 A | |
| L14-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 14-Oct-14 A | |
| I-5032 | RFI 715.1 - Additional Site Paving Per City | 1 | 0 | 14-Oct-14 A | 29-Oct-14 A | |
| L16-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L15-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 15-Oct-14 A | 17-Oct-14 A | |
| L15-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 15-Oct-14 A | |
| SW-2206 | Zone 2 - Grade for curb and gutter | 2 | 0 | 16-Oct-14 A | 20-Oct-14 A | |
| I-5598 | Resolve FCC hard lid ceiling issue (RFI 734) | 1 | 0 | 16-Oct-14 A | 16-Nov-14 A | |

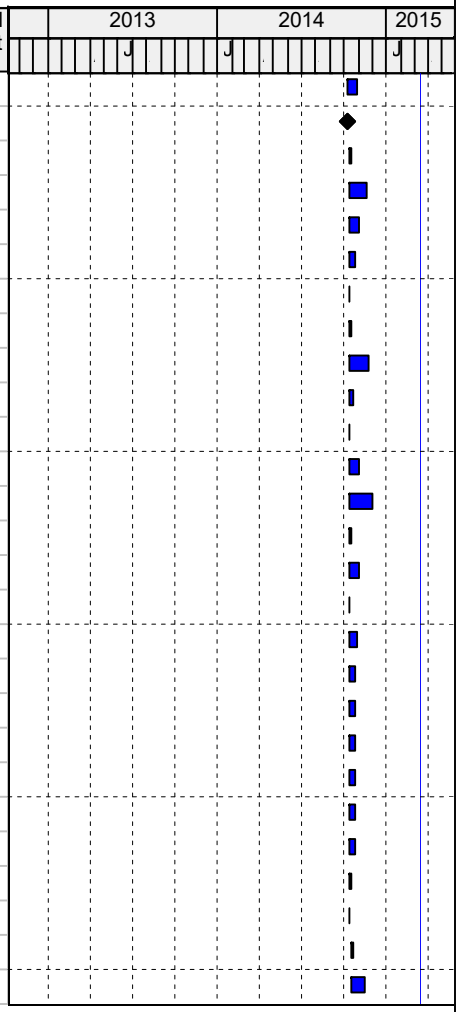



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ASI57 | ASI No. 57 - MDP Electrical Revisions Rev. 22 | 0 | 0 | 17-Oct-14 A | | |
| MPP-1000 | Podium - Install W/S/N Elevations (Elev 1-5, 6,9-19,2 | 10 | 0 | 20-Oct-14 A | 10-Dec-14 A | |
| L06-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 20-Oct-14 A | 23-Oct-14 A | |
| LL2-8106a | LL2, Garage - Pinned Insulation (except at ramp) | 4 | 0 | 20-Oct-14 A | 04-Dec-14 A | |
| L1B-8102d | GWB Hang (Walls) & Inspection - Main Ballroom East | 1 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| SW-2114 | Zone 1 - FRP curb and gutter | 2 | 0 | 20-Oct-14 A | 14-Nov-14 A | |
| RF-4044 | Ballroom Roof - Install metal coping | 3 | 0 | 20-Oct-14 A | 13-Nov-14 A | |
| L08-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 21-Oct-14 A | 23-Oct-14 A | |
| MPT-1018 | Tower - Install Roof Penthouse (Elev 36b,37,38.39) | 5 | 0 | 21-Oct-14 A | 05-Dec-14 A | |
| L11-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2208 | Zone 2 - FRP curb and gutter | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2304 | Zone 3 - FRP curb and gutter | 3 | 0 | 21-Oct-14 A | 02-Dec-14 A | |
| L15-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L06-8130 | Install Door Hardware | 3 | 0 | 21-Oct-14 A | 03-Nov-14 A | |
| I-5100 | Resolve changes (ASI's and RFI's) | 1 | 0 | 21-Oct-14 A | 07-Jan-15 A | |
| L03-8634 | Pool - Install reinforcing steel & inspect | 5 | 0 | 22-Oct-14 A | 30-Oct-14 A | |
| MPT-1016 | Tower - Install N/S Wing, S. End W. of Manlift (Elev 2 | 5 | 0 | 22-Oct-14 A | 05-Dec-14 A | |
| SW-2116 | Zone 1 - Fine grade for sidewalk | 3 | 0 | 22-Oct-14 A | 09-Mar-15 A | |
| LL4-8106 | LL4 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| LL3-8106 | LL3 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L14-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L08-8130 | Install Door Hardware | 3 | 0 | 22-Oct-14 A | 04-Nov-14 A | |
| L07-8130 | Install Door Hardware | 3 | 0 | 22-Oct-14 A | 03-Nov-14 A | |
| ASI54 | ASI No. 54 - Architectural Revisions for Lobby and Clc | 0 | 0 | 22-Oct-14 A | | |
| ASI55 | ASI No. 55 - Kay Lang Interior Concierge and Lobby | 0 | 0 | 22-Oct-14 A | | |
| L03-8606 | L3 Pool - HVAC R/I | 3 | 0 | 23-Oct-14 A | 27-Oct-14 A | |
| L09-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 23-Oct-14 A | 03-Nov-14 A | |

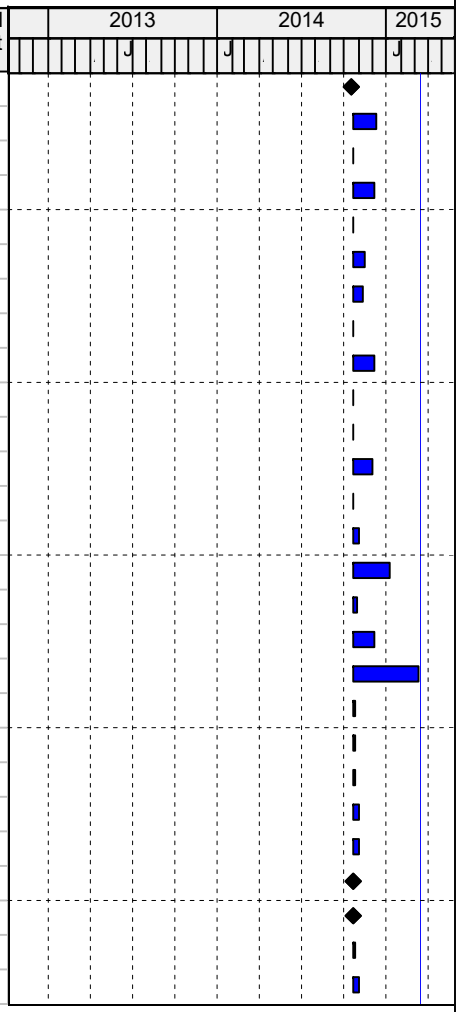



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| LL2-2078 | Generator - Install fuel fill control wiring | 2 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| I-2950 | Kitchen Hood Type 1 impact (COB correction notice, I | 1 | 0 | 23-Oct-14 A | 21-Dec-14 A | |
| RF-4050 | Roof at Manlift - Erect steel | 1 | 0 | 24-Oct-14 A | 24-Oct-14 A | |
| CO-7204 | Cx - Gas Service established | 0 | 0 | | 24-Oct-14 A | |
| I-5900 | Owner select color for Porte Cochere drive concrete | 20 | 0 | 24-Oct-14 A | 11-Mar-15 A | |
| L1BOH2-8102 | GWB Hang (Walls) | 4 | 0 | 27-Oct-14 A | 07-Nov-14 A | |
| L04-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 27-Oct-14 A | 12-Nov-14 A | |
| RF-4052 | Roof at Manlift - Framing/sheathing/air barrier (inspec | 4 | 0 | 27-Oct-14 A | 30-Oct-14 A | |
| LL2-2080 | Generator - Complete generator accessories (battery) | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| LL2-2082 | Generator - Cx fuel fill | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| L09-8130 | Install Door Hardware | 3 | 0 | 28-Oct-14 A | 04-Nov-14 A | |
| CO-7158 | Generator - Interim electrical inspection | 1 | 0 | 29-Oct-14 A | 29-Oct-14 A | |
| LL2-2070 | LL2 - Generator Room - Generator Ready for Startup | 0 | 0 | | 30-Oct-14 A | |
| LL2-2084 | Generator - Initial fuel fill | 1 | 0 | 30-Oct-14 A | 30-Oct-14 A | |
| CO-7200 | Cx - Penthouse Mechanical Installation Complete | 0 | 0 | | 30-Oct-14 A | |
| EL-6028 | Elev 6 - RFI-761: Response, pricing, complete work (r | 20 | 0 | 30-Oct-14 A | 27-Jan-15 A | |
| L03-8636 | Pool - Shotcrete | 1 | 0 | 31-Oct-14 A | 31-Oct-14 A | |
| RF-4054 | Roof at Manlift - Final mechanical installations | 4 | 0 | 31-Oct-14 A | 05-Nov-14 A | |
| RF-4056 | Roof at Manlift - Final electrical connections | 2 | 0 | 31-Oct-14 A | 05-Nov-14 A | |
| CO-7130 | Fire Alarm - Point-To-Point Wiring | 18 | 0 | 01-Nov-14 A | 06-Feb-15 A | |
| L03-8404 | GWB Hang/Tape Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 14-Nov-14 A | |
| L04-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 14-Nov-14 A | |
| L05-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 17-Nov-14 A | |
| L06-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 17-Nov-14 A | |
| L03-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L04-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |

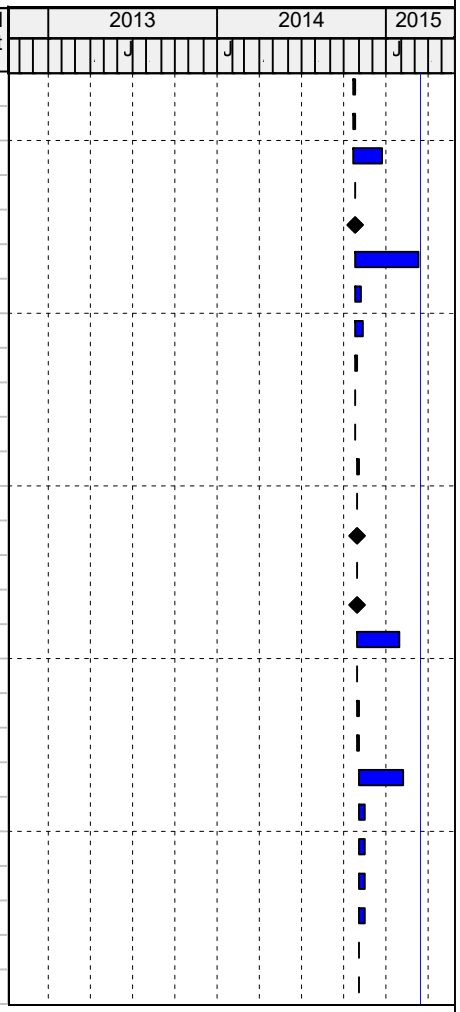



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L06-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L07-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L08-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L09-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L10-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L11-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L12-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L14-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L15-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L16-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L17-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L14-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 03-Nov-14 A | 06-Nov-14 A | |
| MPT-1024 | (A) Caulking - Elevation 41 (east elevation above poo | 7 | 0 | 03-Nov-14 A | 16-Dec-14 A | |
| CO-7206 | Cx - Purge/Prove Gas-Fed Equipment and Feeder Li | 7 | 0 | 03-Nov-14 A | 09-Nov-14 A | |
| I-5200 | Resolve MEP conflicts with ceiling grid (RFIs 783 & 8 | 8 | 3 | 03-Nov-14 A | 18-Mar-15 | 6 |
| I-5040 | RFI 776 - North Sidewalk-Entrance Conflicts | 1 | 0 | 03-Nov-14 A | 18-Dec-14 A | |
| L07-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 17-Nov-14 A | |
| L08-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L09-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L10-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L12-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L11-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 04-Nov-14 A | 15-Dec-14 A | |
| L11-8130 | Install Door Hardware | 3 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L10-8130 | Install Door Hardware | 3 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L11-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 18-Nov-14 A | |
| L12-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 19-Nov-14 A | |

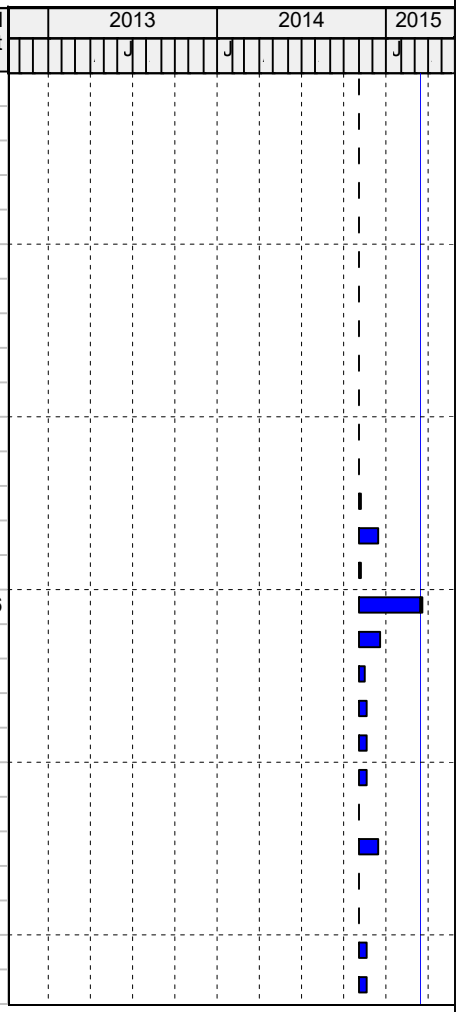



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 19-Nov-14 A | |
| MPP-1010 | Podium - Install East Elevation (Elev 5 & 7) | 7 | 0 | 05-Nov-14 A | 10-Dec-14 A | |
| CO-7162 | Generator - Load bank testing | 1 | 0 | 05-Nov-14 A | 05-Nov-14 A | |
| CO-7202 | Cx - Electrical Internal Bus & LL2-L17 Bus Duct Energ | 0 | 0 | | 05-Nov-14 A | |
| CO-7202a | Cx - Energize normal power distribution | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| I-5036 | RFI 717.1 - Porte Cochere Paving Details | 1 | 0 | 05-Nov-14 A | 26-Nov-14 A | |
| L15-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 19-Nov-14 A | |
| L16-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 20-Nov-14 A | |
| L17-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 20-Nov-14 A | |
| RF-4058 | Roof at Manlift - Install roofing | 2 | 0 | 06-Nov-14 A | 07-Nov-14 A | |
| CO-7164 | Generator - Final electrical inspection | 1 | 0 | 06-Nov-14 A | 06-Nov-14 A | |
| ASI59 | ASI No. 59 - Electrical One-Line Revisions | 0 | 0 | 06-Nov-14 A | | |
| I-5042 | RFI 796 - City Requested Added Scope | 1 | 0 | 06-Nov-14 A | 22-Dec-14 A | |
| I-5046 | RFI 803 - Site Light Bases Layout with Existing Sidew | 1 | 0 | 06-Nov-14 A | 14-Jan-15 A | |
| L15-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 07-Nov-14 A | 12-Nov-14 A | |
| L03-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L03-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L04-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L04-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L05-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L05-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L06-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L06-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L07-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L07-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L08-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L08-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |

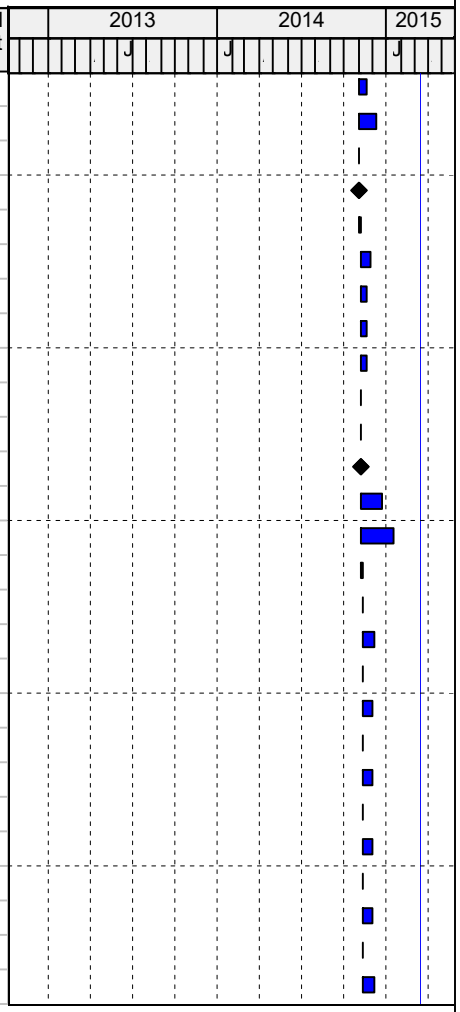



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L09-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L10-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L10-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L11-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L11-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L12-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L12-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L14-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L14-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L15-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L15-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L16-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L16-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L17-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L17-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L05-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| L06-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 10-Nov-14 A | 11-Nov-14 A | |
| MPT-1032 | Tower - Install sign backing NW (Elev 51,52) | 4 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L12-8130 | Install Door Hardware | 3 | 0 | 10-Nov-14 A | 12-Nov-14 A | |
| EL-1230 | Elev 1&2 - Complete hoistway ventilation | 13 | 0 | 10-Nov-14 A | 15-Dec-14 A | |
| EL-1232 | Elev 1&2 - Wire & startup AC split units | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-1234 | Elev 1&2 - Install EMR doors, hardware & labeling | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-3428 | Elev 3&4 - Complete hoistway ventilation | 13 | 0 | 10-Nov-14 A | 15-Dec-14 A | |
| EL-3430 | Elev 3&4 - Wire & startup AC split units | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-3432 | Elev 3&4 - Install EMR doors, hardware & labeling | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-6030 | Elev 6 - Complete fire-rated assemblies at hoistway, l | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |

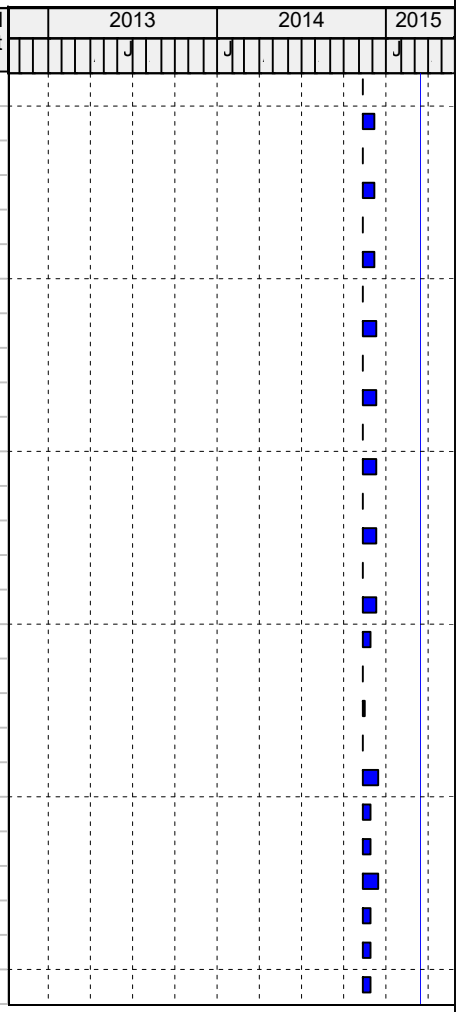



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 11-Nov-14 A | 12-Nov-14 A | |
| L16-8106 | Paint - Accent Walls | 2 | 0 | 11-Nov-14 A | 12-Nov-14 A | |
| L14-8130 | Install Door Hardware | 3 | 0 | 11-Nov-14 A | 13-Nov-14 A | |
| I-5044 | RFI 802 - Landscape Planter & Arch Detail Coordinati | 1 | 0 | 11-Nov-14 A | 18-Nov-14 A | |
| L03-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 12-Nov-14 A | 18-Nov-14 A | |
| SW-2104 | Zone 1 - Install lighting conduit at SE corner | 2 | 0 | 12-Nov-14 A | 14-Nov-14 A | |
| L16-8111 | Paint - Door Jambs | 2 | 0 | 12-Nov-14 A | 13-Nov-14 A | |
| EL-6010i | Elev 6 - Pit Slab Correction (form/pour/strip/clean) | 10 | 0 | 12-Nov-14 A | 26-Nov-14 A | |
| SW-2024 | Zone 4 - FRP Porte Cochere planter & bench | 6 | 0 | 12-Nov-14 A | 04-Dec-14 A | |
| L08-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| SW-2109 | Zone 1 - Install irrigation sleeves | 2 | 0 | 13-Nov-14 A | 14-Nov-14 A | |
| MPT-1026 | (C) Caulking - Elevation 47 (north elevation, east half | 10 | 0 | 13-Nov-14 A | 19-Dec-14 A | |
| L16-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| L15-8130 | Install Door Hardware | 3 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| ASI56 | ASI No. 56 - Interior Design Millwork and Finish Chan | 0 | 0 | 13-Nov-14 A | | |
| L04-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 14-Nov-14 A | 19-Nov-14 A | |
| SW-2203 | Zone 2 - Install irrigation sleeves | 2 | 0 | 14-Nov-14 A | 08-Jan-15 A | |
| L1B-8120 | Install operable partitions | 3 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| LL1-Z3-8340 | Install walk-in cooler/freezer (BY OTHERS) | 5 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| SW-2316 | Zone 3 - Demolish manlift shack and base | 5 | 0 | 17-Nov-14 A | 20-Nov-14 A | |
| I-1610 | Enclosure at manlift - Install exterior wall panels & ins | 5 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| L04-8140 | Install window sills | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| L03-8140x | Install window sills | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| L16-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| SW-2014 | Porte Cochere - Electrical rough-in | 5 | 0 | 17-Nov-14 A | 08-Dec-14 A | |
| I-5600 | Lower heat pump and install access panels (RFI 734) | 13 | 0 | 17-Nov-14 A | 09-Jan-15 A | |
| LL1-Z3-FCC26 | Program FACP & Stand-Up System | 20 | 0 | 17-Nov-14 A | 22-Jan-15 A | |

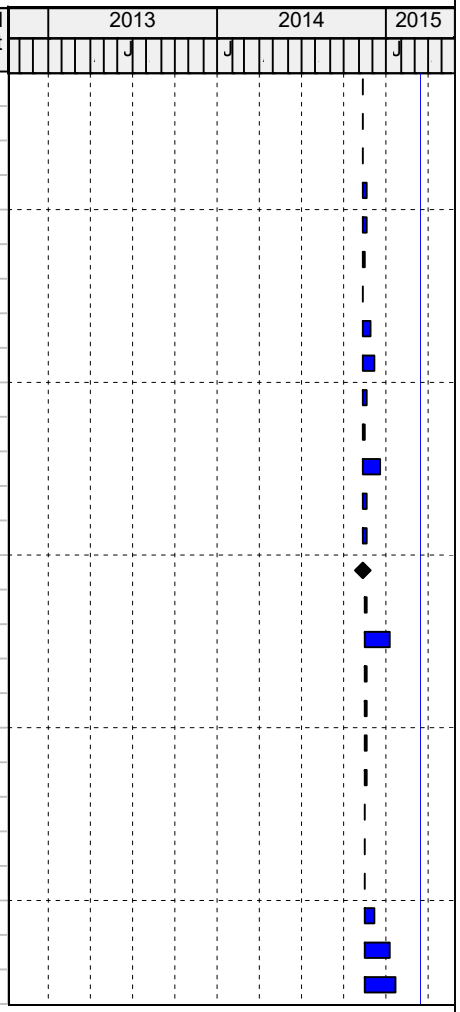



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8140 | Install window sills | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L05-8140 | Install window sills | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| I-5048 | RFI 805 - City Approved Public ROW Irrigation Lines M | 1 | 0 | 18-Nov-14 A | 05-Dec-14 A | |
| L05-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 19-Nov-14 A | 22-Dec-14 A | |
| L16-8130 | Install Door Hardware | 3 | 0 | 19-Nov-14 A | 02-Dec-14 A | |
| L08-8140 | Install window sills | 2 | 0 | 19-Nov-14 A | 19-Nov-14 A | |
| L07-8140 | Install window sills | 2 | 0 | 19-Nov-14 A | 19-Nov-14 A | |
| I-1616 | Enclosure at manlift - Patch/repair concrete shear wal | 3 | 0 | 19-Nov-14 A | 21-Nov-14 A | |
| ASI58 | ASI No. 58 - Level 1 Valet Phone and POS Locations | 0 | 0 | 19-Nov-14 A | | |
| ASI59ca | ASI No. 59 - Electrical One-Line Revisions (City Appro | 0 | 0 | 19-Nov-14 A | | |
| L10-8140 | Install window sills | 2 | 0 | 20-Nov-14 A | 20-Nov-14 A | |
| L09-8140 | Install window sills | 2 | 0 | 20-Nov-14 A | 20-Nov-14 A | |
| I-1622 | Manlift finishes - Install windows & caulk | 4 | 0 | 20-Nov-14 A | 03-Dec-14 A | |
| LL2-2060 | LL2 - Paint Laundry Room | 3 | 0 | 21-Nov-14 A | 24-Nov-14 A | |
| L03-8616 | L3 Pool - GWB above ceiling | 2 | 0 | 21-Nov-14 A | 22-Nov-14 A | |
| LL1-Z3-8342 | Final connections at walk-in cooler/freezer | 2 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L1K-8340 | Install walk-in cooler/freezer (BY OTHERS) | 2 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L10-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| L16-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| SW-2110 | Zone 1 - Adjust utilities structures | 5 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| SW-2214 | Zone 2 - Adjust utilities structures | 2 | 0 | 24-Nov-14 A | 25-Nov-14 A | |
| MPT-1030 | Tower - Install sign backing NE (Elev 44) | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| SW-2012 | Porte Cochere - Install cornice[DELETED SEE REV M | 8 | 0 | 24-Nov-14 A | 05-Dec-14 A | |
| L03-8650 | L3 Pool - Build scaffold at pool pit | 2 | 0 | 24-Nov-14 A | 25-Nov-14 A | |
| EL-6032 | Elev 6 - Install pit ladder | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| EL-6034 | Elev 6 - Install pit jack & hoistway pistons; connect hy | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| L06-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 25-Nov-14 A | 22-Dec-14 A | |

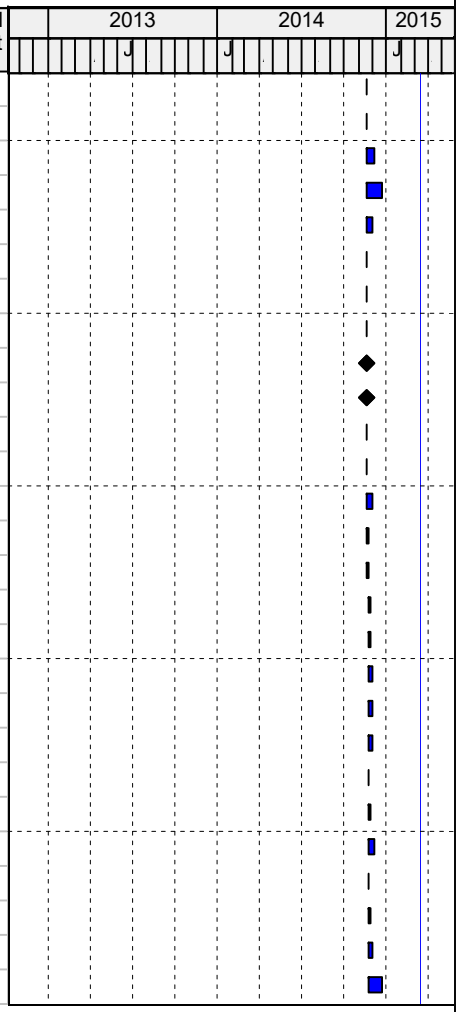



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8104a | L2 - Int Painting - South Half | 2 | 0 | 25-Nov-14 A | 26-Nov-14 A | |
| SW-2016 | Porte Cochere - Complete framing | 3 | 0 | 25-Nov-14 A | 01-Dec-14 A | |
| LL2-2096 | LL2 - Install FRP at Laundry Room | 8 | 0 | 25-Nov-14 A | 05-Dec-14 A | |
| I-1602 | Enclosure at manlift - Install shear wall clips and inspe | 4 | 0 | 26-Nov-14 A | 05-Dec-14 A | |
| L07-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| SW-2318 | Zone 3 - Install catch basin | 1 | 0 | 26-Nov-14 A | 26-Nov-14 A | |
| L03-8652 | L3 Pool - Frame ceiling | 4 | 0 | 26-Nov-14 A | 04-Dec-14 A | |
| I-5052 | RFI 819 - Flagpole Locations | 1 | 0 | 26-Nov-14 A | 30-Dec-14 A | |
| I-5050 | RFI 818 - 111th East Elevation Hardscape Vertical Dif | 1 | 0 | 26-Nov-14 A | 29-Dec-14 A | |
| L03-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L04-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L05-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L06-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L07-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L09-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L10-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L11-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L12-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L14-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L15-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L16-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L17-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 01-Dec-14 A | 04-Dec-14 A | |
| L02-6016a | L2 - Electrical Room Buildout | 5 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| L03-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L04-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |

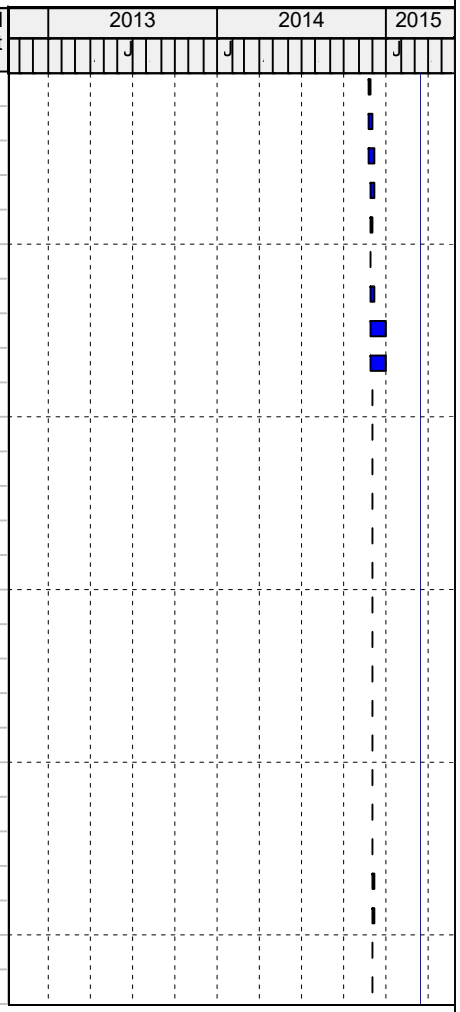



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L06-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L07-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L09-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L10-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L11-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L12-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L14-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L15-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L16-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L17-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| SW-2210 | Zone 2 - Fine grade for sidewalk | 5 | 0 | 01-Dec-14 A | 08-Jan-15 A | |
| RF-4040 | L2.5 Horseshoe - Install sheet metal capping[DELETI | 3 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| MPT-1042 | Enclosure at manlift - air barrier & inspect | 5 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| CO-7208 | Cx - Start-Up Pumps | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| CO-7210 | Cx - Start-Up VFD's | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| L17-8106 | Paint - Accent Walls | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| LL4-8116 | LL4 - Install ACT grid [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL3-8116 | LL3 - Install ACT grid [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| I-1630 | Manlift finishes - Framing, corridor ceilings & inspect | 4 | 0 | 01-Dec-14 A | 09-Dec-14 A | |
| EL-6036 | Elev 6 - Install shunt trip breaker | 5 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| L17-8111 | Paint - Door Jambs | 2 | 0 | 02-Dec-14 A | 03-Dec-14 A | |
| SW-2018 | Porte Cochere - GWB hang/tape | 3 | 0 | 02-Dec-14 A | 09-Dec-14 A | |
| L03-8654 | L3 Pool - HVAC drops at ceiling & inspect | 3 | 0 | 02-Dec-14 A | 05-Dec-14 A | |
| L11-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 03-Dec-14 A | 08-Dec-14 A | |
| SW-2308 | Zone 3 - Install site lighting | 5 | 0 | 03-Dec-14 A | 04-Dec-14 A | |

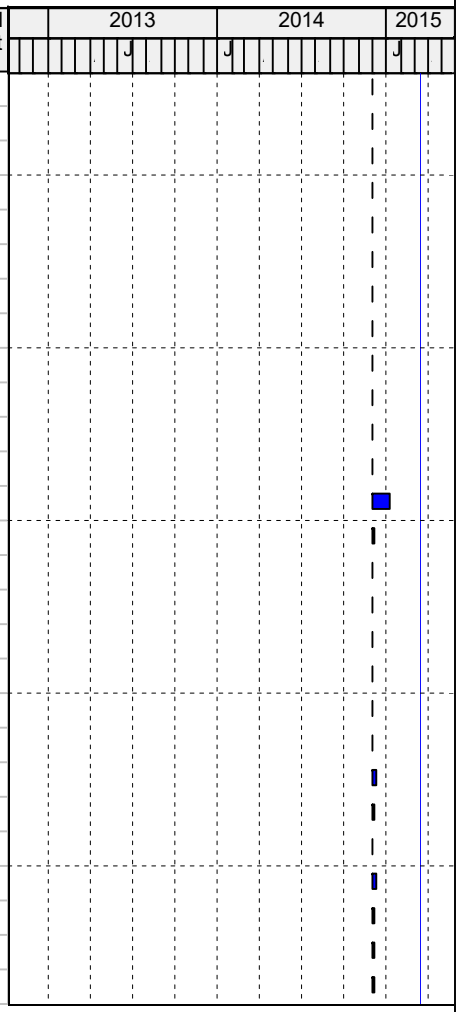



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 03-Dec-14 A | 15-Dec-14 A | |
| I-1632 | Manlift finishes - Electrical rough-in & inspect | 2 | 0 | 03-Dec-14 A | 10-Dec-14 A | |
| SW-2028 | Zone 4 - Scan Porte Cochere deck | 2 | 0 | 04-Dec-14 A | 05-Dec-14 A | |
| I-1624 | Manlift finishes - Install batt insulation & inspect | 2 | 0 | 04-Dec-14 A | 04-Dec-14 A | |
| I-1626 | Manlift finishes - Shim window openings | 2 | 0 | 04-Dec-14 A | 05-Dec-14 A | |
| I-1628 | Manlift finishes - Install vapor barrier & inspect | 2 | 0 | 04-Dec-14 A | 08-Dec-14 A | |
| I-5054 | RFI 832.1 - South Elevation Emergency Exit with Side | 1 | 0 | 04-Dec-14 A | 18-Dec-14 A | |
| I-1608 | Tower - Install N/S Wing, S. End at manlift (Elev 32) [I | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1012 | Tower - Install N/S Wing, S. End E. Side Concrete (El | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| PC-4012 | Porte Cochere - Install sheet metal capping[DELETEI | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4046 | Tower Roof - Install sheet metal capping[DELETED S | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4060 | Roof at Manlift - Install corrugated metal panels[DELE | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4062 | Roof at Manlift - Install sheet metal capping[DELETEI | 2 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4064 | Pool Green Roof - Install sheet metal capping[DELET | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1040 | Tower - Install N/S Wing, S, End (Elev 30)[DELETED | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1044 | Enclosure at manlift - Install sign backing south[DELE | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1612 | Enclosure at manlift - Caulking[DELETED SEE REV M | 8 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1614 | Enclosure at manlift - Install rigid insulation at shear w | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1618 | Enclosure at manlift - Install framing at shear wall[DEI | 5 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1620 | Enclosure at manlift - Install hat channel over framing | 5 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| L03-8656 | L3 Pool - Electrical rough-in at ceiling & inspect | 3 | 0 | 05-Dec-14 A | 19-Dec-14 A | |
| I-5058 | RFI 834 - NE Retaining Wall Design Clarifications | 1 | 0 | 05-Dec-14 A | 23-Dec-14 A | |
| I-5062 | RFI 835 - NW Planter Wall Drainage | 1 | 0 | 05-Dec-14 A | 10-Dec-14 A | |
| L1K-8344 | Set kitchen hoods | 8 | 0 | 06-Dec-14 A | 21-Dec-14 A | |
| L12-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L03-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |
| L04-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |

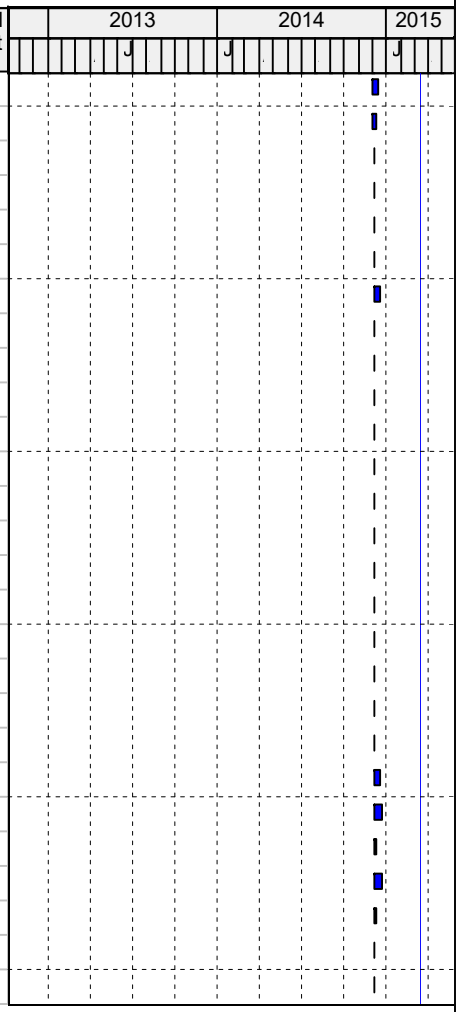



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |
| SW-2312 | Zone 3 - Fine grade for sidewalk | 3 | 0 | 08-Dec-14 A | 08-Jan-15 A | |
| RF-4042 | Pool Roof - Install metal coping at high roof | 2 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L17-8130 | Install Door Hardware | 3 | 0 | 08-Dec-14 A | 11-Dec-14 A | |
| L09-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L03-8658 | L3 Pool - Fire sprinkler drops at ceiling & inspect | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| LL2-8140 | LL2 - Install vinyl wall coverings | 2 | 0 | 08-Dec-14 A | 24-Dec-14 A | |
| L04-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L05-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L07-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L08-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L14-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L15-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 09-Dec-14 A | 12-Dec-14 A | |
| L03-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L07-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L08-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L04-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L05-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L07-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L08-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |

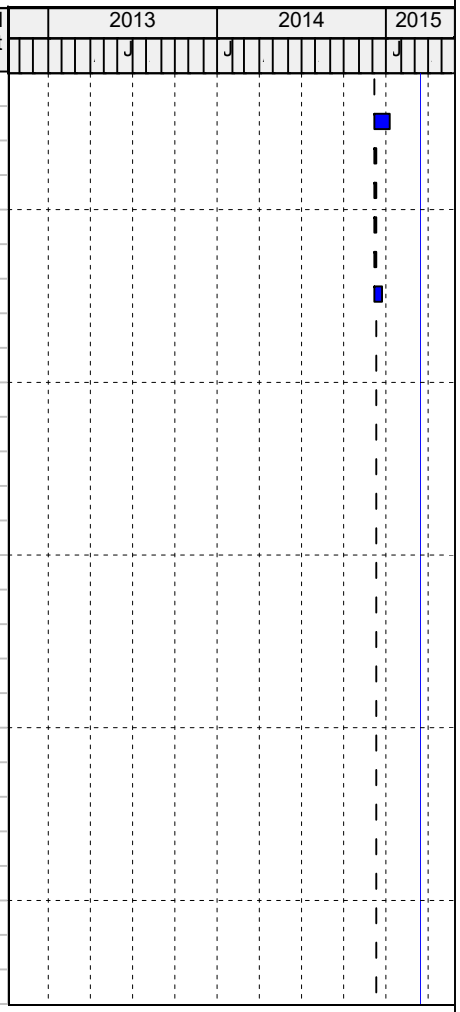



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| RF-4072 | Pool Roof - Install metal coping | 3 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L17-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 09-Dec-14 A | 12-Dec-14 A | |
| L07-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 09-Dec-14 A | 29-Dec-14 A | |
| L06-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 09-Dec-14 A | 24-Dec-14 A | |
| I-1604 | Manlift finishes - GWB, hang walls | 2 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L07-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L08-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 16-Dec-14 A | |
| L11-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L12-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L14-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L15-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L16-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L17-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| LL2E-8340 | LL2 - Install walk-in cooler/freezer (BY OTHERS) | 5 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L10-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 10-Dec-14 A | 17-Dec-14 A | |
| L09-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L10-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L11-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L11-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L12-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L14-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L15-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L16-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L17-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L08-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 10-Dec-14 A | 29-Dec-14 A | |
| I-1634 | Manlift finishes - GWB, hang ceilings | 2 | 0 | 10-Dec-14 A | 16-Dec-14 A | |

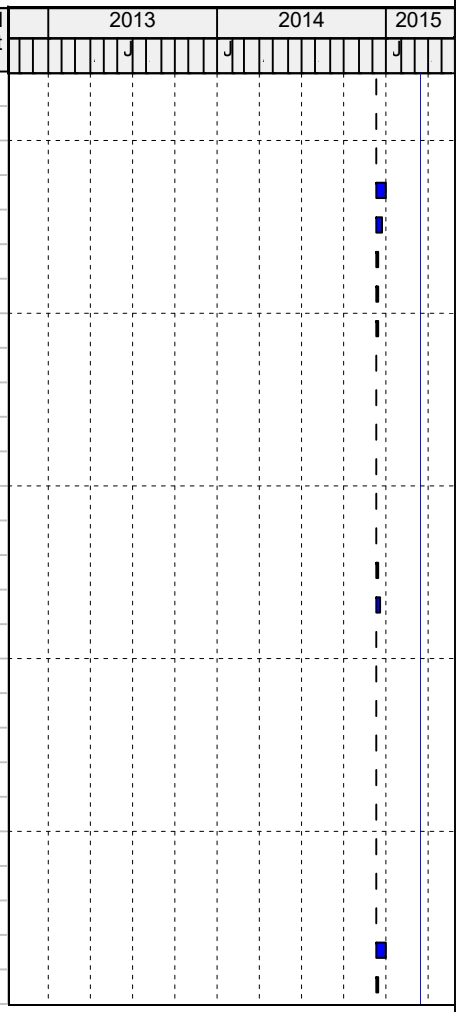



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L14-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L15-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L03-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L04-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| MPT-1034 | (A) Elevation 52 (west elevation, north end, L3-L18) | 4 | 0 | 11-Dec-14 A | 16-Dec-14 A | |
| MPT-1036 | (B) Elevation 45/46 (north elevation, east end, L3-L1 | 5 | 0 | 11-Dec-14 A | 19-Dec-14 A | |
| L16-7030 | Paint | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L17-7030 | Paint | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L05-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L06-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| MPT-1066 | Tower Sign, East (El. 32) - Install backing | 3 | 0 | 12-Dec-14 A | 22-Dec-14 A | |
| MPT-1076 | (B) Caulking - Elevation 51 (north elevation, west half | 10 | 0 | 12-Dec-14 A | 19-Dec-14 A | |
| L04-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L04-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L07-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L08-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L09-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L14-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L15-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L17-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 16-Dec-14 A | |
| L04-7042 | Install Tile Flooring (x41) | 2 | 0 | 15-Dec-14 A | 24-Dec-14 A | |
| L05-7042 | Install Tile Flooring (x41) | 2 | 0 | 15-Dec-14 A | 24-Dec-14 A | |

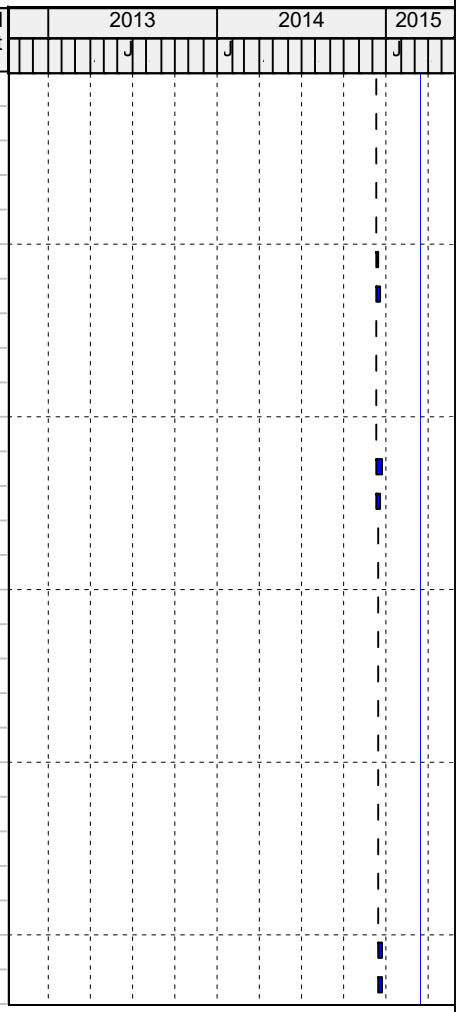



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8102a | LL4 - GWB Tape/Finish | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| LL3-8102a | LL3 - GWB Tape/Finish | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| L03-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L04-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L07-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L08-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L09-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L10-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| CO-7126 | Fire pump test pre-planning complete (see checklist) | 0 | 0 | | 15-Dec-14 A | |
| LL1-Z3-6034 | COB Correction - Add ceiling access panels in Food F | 10 | 0 | 15-Dec-14 A | 26-Jan-15 A | |
| L03-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| L05-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L09-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L10-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L10-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L11-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L11-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L14-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L15-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L16-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L17-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| LL2E-8342 | LL2 - Final connections at walk-in cooler/freezer | 5 | 0 | 16-Dec-14 A | 05-Jan-15 A | |
| L11-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 16-Dec-14 A | 18-Dec-14 A | |

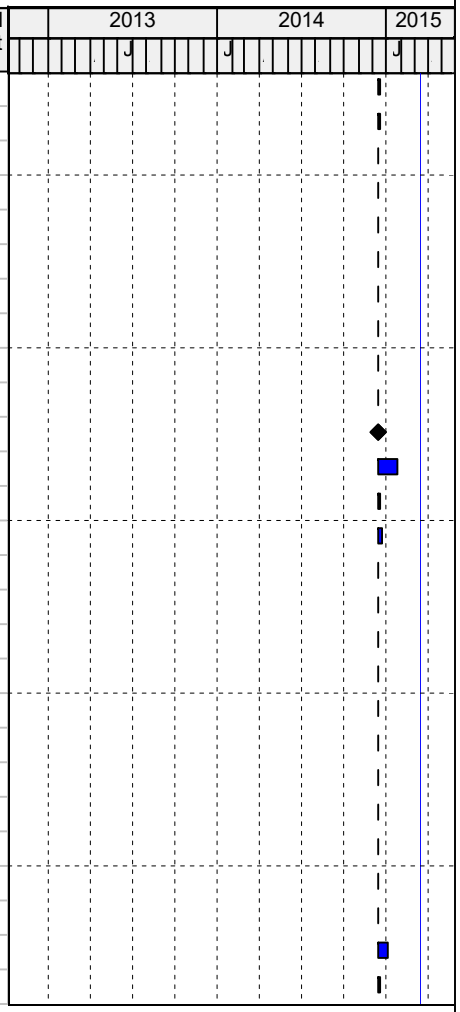



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8201 | Corridors - Install ACT Grid | 2 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L06-7042 | Install Tile Flooring (x41) | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L07-7042 | Install Tile Flooring (x41) | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| LL1-Z2-8102a | GWB Hang (Ceilings) & Inspection | 3 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L11-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L14-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L15-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L16-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L17-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| CO-7128 | Run fire pump test | 2 | 0 | 16-Dec-14 A | 17-Dec-14 A | |
| L09-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 16-Dec-14 A | 30-Dec-14 A | |
| SW-2026 | Zone 4 - FRP NW planter | 5 | 0 | 16-Dec-14 A | 05-Jan-15 A | |
| I-5370 | (S) Resolve south tower sign backing (RFI 844) | 5 | 0 | 16-Dec-14 A | 09-Jan-15 A | |
| L03-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 22-Dec-14 A | |
| L04-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 23-Dec-14 A | |
| L06-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 29-Dec-14 A | |
| L07-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 30-Dec-14 A | |
| L08-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 31-Dec-14 A | |
| L09-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 05-Jan-15 A | |
| L14-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L15-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L16-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L17-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L08-7042 | Install Tile Flooring (x41) | 2 | 0 | 17-Dec-14 A | 24-Dec-14 A | |
| L09-7042 | Install Tile Flooring (x41) | 2 | 0 | 17-Dec-14 A | 24-Dec-14 A | |
| L04-7136 | Install Door and Hardware | 1 | 0 | 17-Dec-14 A | 17-Dec-14 A | |

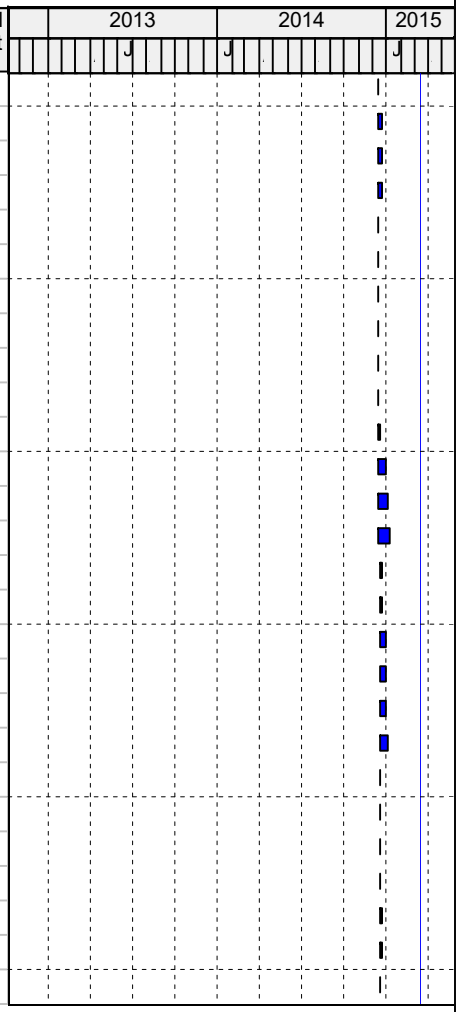



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 17-Dec-14 A | 29-Dec-14 A | |
| MPT-1046 | (A) Elevation 26/27/53 (west elevation, south of 52, L | 3 | 0 | 17-Dec-14 A | 18-Dec-14 A | |
| MPT-1057 | (S) Elevation 32 framing (south elevation, east of mai | 5 | 0 | 17-Dec-14 A | 19-Jan-15 A | |
| MPT-1080 | (A) Caulking - Elevation 44 (east elevation above poo | 8 | 0 | 17-Dec-14 A | 22-Dec-14 A | |
| LL1-Z2-8108 | Framing, ceiling clouds (incl. inspection) | 5 | 0 | 17-Dec-14 A | 22-Jan-15 A | |
| MPP-1006 | (C) Install Level 3 cornice metal (north, west & south) | 6 | 0 | 18-Dec-14 A | 30-Jan-15 A | |
| L10-7042 | Install Tile Flooring (x41) | 2 | 0 | 18-Dec-14 A | 24-Dec-14 A | |
| L11-7042 | Install Tile Flooring (x41) | 2 | 0 | 18-Dec-14 A | 24-Dec-14 A | |
| L12-7042 | Install Tile Flooring (x41) | 2 | 0 | 19-Dec-14 A | 24-Dec-14 A | |
| L14-7042 | Install Tile Flooring (x41) | 2 | 0 | 19-Dec-14 A | 24-Dec-14 A | |
| MPT-1048 | (B) Elevation 37 (penthouse east) | 3 | 0 | 19-Dec-14 A | 20-Dec-14 A | |
| I-5000 | Resolve RFI's and site work changes (new drawings) · | 10 | 0 | 19-Dec-14 A | 02-Mar-15 A | |
| I-5002 | Resolve RFI's and site work changes (new drawings) · | 20 | 0 | 19-Dec-14 A | 09-Feb-15 A | |
| I-5003 | Resolve RFI's and site work changes (new drawings) · | 10 | 0 | 19-Dec-14 A | 02-Mar-15 A | |
| I-5004 | Resolve RFI's and site work changes (new drawings) · | 1 | 0 | 19-Dec-14 A | 16-Jan-15 A | |
| I-5064 | RFI 848 - Lighting at Flagpole Locations | 1 | 0 | 19-Dec-14 A | 14-Jan-15 A | |
| L03-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 22-Dec-14 A | 22-Dec-14 A | |
| L07-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L17-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| CO-7212 | Cx - Start-Up Boilers | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L17-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L08-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L07-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L06-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L05-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L04-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 22-Dec-14 A | |
| I-1636 | Manlift finishes - GWB, tape & finish | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |

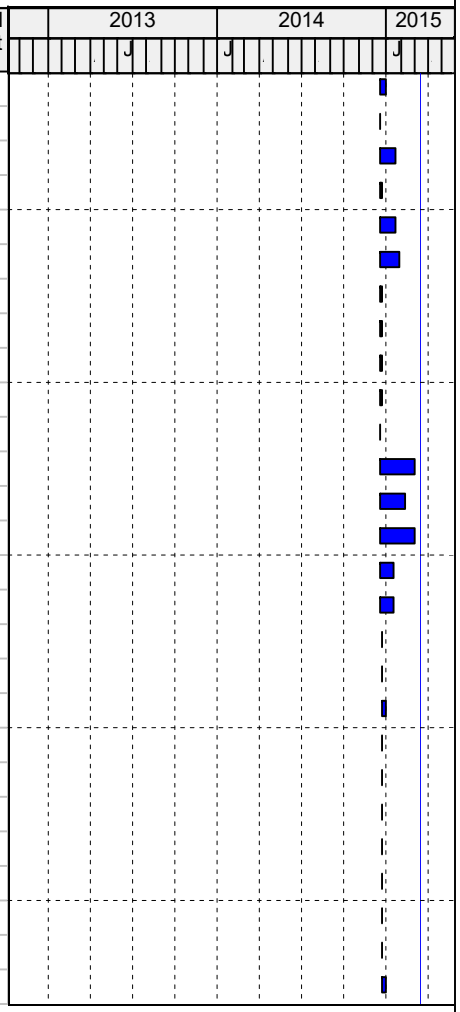



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6038 | Elev 6 - Rough-in call boxes & lanterns | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| EL-6052 | Elev 6 - Complete hoistway ventilation | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| MPT-1078 | (C) Caulking - Elevation 37/38/39 (penthouse) | 4 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| MPT-1086 | (A) Caulking - Elevation 45/46 (north elevation, east e | 7 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| MPT-1088 | (B) Caulking - Elevation 52/53/26/27 (west elevation, | 11 | 0 | 22-Dec-14 A | 02-Jan-15 A | |
| MPP-1044 | Caulking - Elevation 9/10/11/12/13 (upper ballroom) | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| MPP-1046 | Caulking - Elevation 5/6 (east elevation, south end) | 8 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| I-5068 | RFI 857 - South Elevation Landscape & Irrigation Re( | 1 | 0 | 22-Dec-14 A | 07-Jan-15 A | |
| I-5070 | RFI 858 - North Elevation Landscape & Irrigation Req | 1 | 0 | 22-Dec-14 A | 07-Jan-15 A | |
| I-5072 | RFI 859 - Additional Curbs at Openings (see RFI 776) | 1 | 0 | 22-Dec-14 A | 07-Jan-15 A | |
| L03-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L03-7032 | Install VCT Flooring (x42) | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L08-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L10-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L09-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| ASI62 | ASI No. 62 - Civil Site Grading Revisions | 0 | 0 | 23-Dec-14 A | | |
| I-5074 | RFI 860 - SE Corner Hardscape Additional Clarificatio | 1 | 0 | 23-Dec-14 A | 07-Jan-15 A | |
| L09-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 24-Dec-14 A | 29-Dec-14 A | |
| L03-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 31-Dec-14 A | |
| L15-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L16-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L17-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L04-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L05-7136 | Install Door and Hardware | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L10-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L17-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| LL1-Z3-8202 | Install FRP wall coverings | 4 | 0 | 29-Dec-14 A | 06-Jan-15 A | |

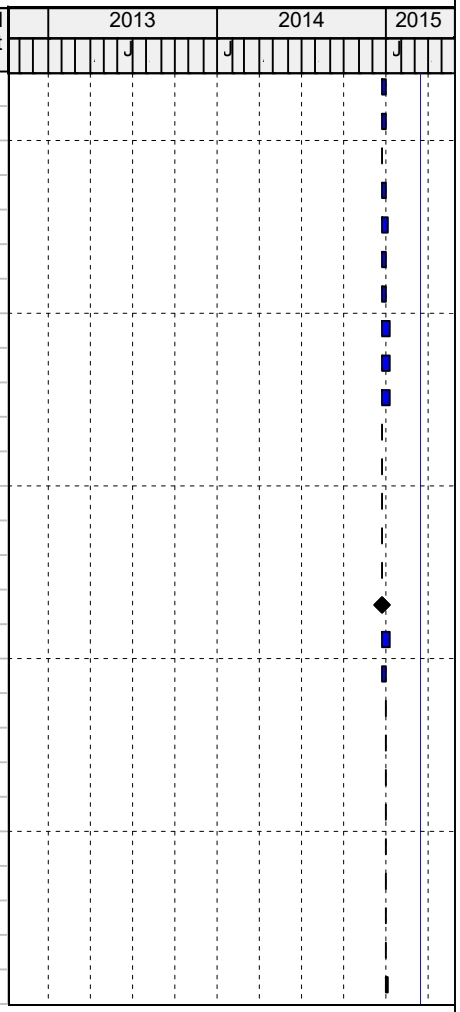



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L05-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L06-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L07-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L08-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L09-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L10-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL2-8130 | LL2 - Install ceiling grid | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| I-5300 | Heat Pump Revision - demo existing ceiling framing | 2 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L12-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 30-Dec-14 A | 05-Jan-15 A | |
| L06-7136 | Install Door and Hardware | 1 | 0 | 30-Dec-14 A | 30-Dec-14 A | |
| L11-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 30-Dec-14 A | 31-Dec-14 A | |
| I-5302 | Heat Pump Revision - rework MEP at celing | 5 | 0 | 30-Dec-14 A | 12-Jan-15 A | |
| I-1606 | Manlift finishes - Prime & paint | 4 | 0 | 31-Dec-14 A | 06-Jan-15 A | |
| L07-7136 | Install Door and Hardware | 1 | 0 | 31-Dec-14 A | 31-Dec-14 A | |
| L12-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 31-Dec-14 A | 05-Jan-15 A | |
| CO-7214 | Cx - Flush & Fill HVAC Hydronics Systems | 5 | 0 | 02-Jan-15 A | 05-Jan-15 A | |
| MPP-1032 | (C) Elevation 23/24/25 (Porte Cochere north, below c | 5 | 0 | 02-Jan-15 A | 19-Jan-15 A | |
| L1BOH2-8215 | GWB tape & finish walls & ceilings | 7 | 0 | 05-Jan-15 A | 02-Mar-15 A | |
| L10-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| L11-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 13-Jan-15 A | |
| L12-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 13-Jan-15 A | |
| L14-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| L16-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L04-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L05-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L06-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |

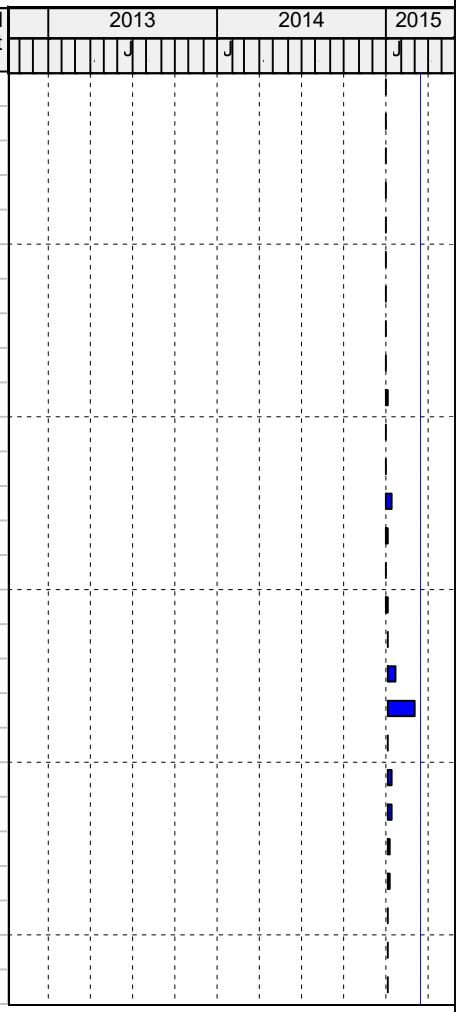



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| L06-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L07-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L08-7136 | Install Door and Hardware | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L08-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L09-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L10-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L14-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| SW-2314 | Zone 3 - FRP sidewalk | 5 | 0 | 05-Jan-15 A | 16-Feb-15 A | |
| L10-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 05-Jan-15 A | 27-Jan-15 A | |
| CO-7240 | Cx - Heat Pump Start-Up - Levels 3 & 4 | 5 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| SW-2220 | Zone 2 - FRP curb/gutter at NW corner | 4 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| MPT-1054 | Complete Elevation 30 (south elevation, west of man | 5 | 1 | 05-Jan-15 A | 16-Mar-15 | 35 |
| MPP-1028 | (C) Tapered pilasters, west | 3 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| MPP-1030 | (C) Tapered pilasters, east | 3 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| LL2-8142 | HVAC drops/trim to grid | 3 | 0 | 05-Jan-15 A | 19-Jan-15 A | |
| L1L-8216 | Complete electrical/fire alarm drops @ ceilings | 5 | 0 | 05-Jan-15 A | 08-Jan-15 A | |
| L1BOH2-8217 | GWB hang ceilings and at heat pumps | 10 | 0 | 05-Jan-15 A | 29-Jan-15 A | |
| L1L-8222 | Complete HVAC drops @ ceilings | 5 | 0 | 05-Jan-15 A | 23-Jan-15 A | |
| L1L-8224 | Complete fire sprinkler drops @ ceilings | 5 | 0 | 05-Jan-15 A | 08-Jan-15 A | |
| L1L-8254 | Complete electrical rough-in at walls | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| I-5350 | Fabricate & install new hydraulic ram | 30 | 0 | 05-Jan-15 A | 29-Jan-15 A | |
| SW-2226 | Zone 2 - Procure light poles and replacement luminai | 30 | 25 | 05-Jan-15 A | 17-Apr-15 | 11 |
| LL1-8120 | Complete GWB tape & finish in corridors | 7 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| L1K-8108 | Complete kitchen hood installation and fire blanket wi | 10 | 0 | 05-Jan-15 A | 05-Feb-15 A | |
| L1K-8110 | Complete MEP rough-in above ceiling | 10 | 0 | 05-Jan-15 A | 05-Feb-15 A | |
| L1B-8122 | Framing, complete ceiling at corridors | 5 | 0 | 05-Jan-15 A | 13-Jan-15 A | |

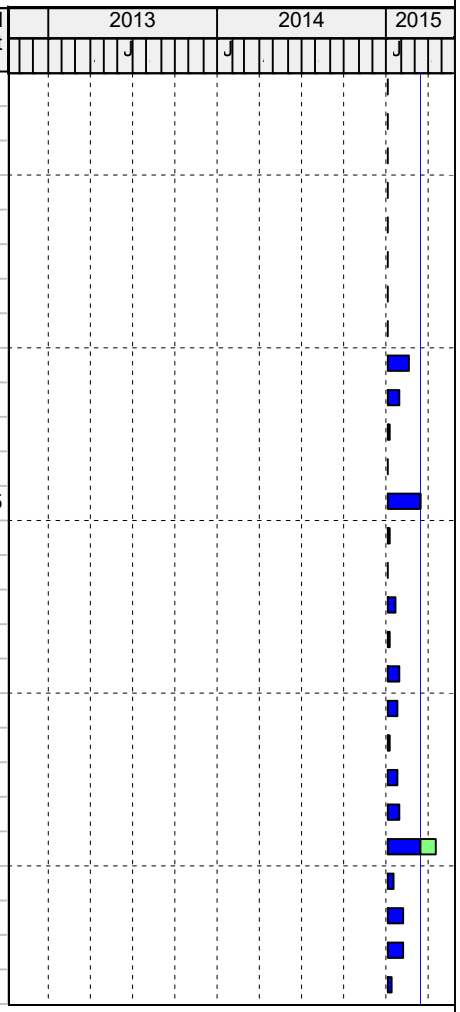



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-5102 | Bar lighting layout - resolve conflicts (RFI) | 7 | 0 | 05-Jan-15 A | 19-Jan-15 A | |
| I-5110 | Bar radius ceiling - resolve framing issues | 5 | 0 | 05-Jan-15 A | 14-Jan-15 A | |
| I-5120 | Dining feature wall - resolve design issues | 7 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| L02-8178 | Complete heat pump enclosures | 5 | 0 | 05-Jan-15 A | 12-Jan-15 A | |
| I-5850 | Owner provide revised lighting layout | 10 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| I-5130 | Bar plumbing relocation - resolve conflicts | 25 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| I-5140 | Damper at BPF #8 - resolve conflicts | 30 | 0 | 05-Jan-15 A | 29-Jan-15 A | |
| I-5150 | Sprinkler pipe furring - resolve conflicts | 15 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| I-5160 | ASI 63 electrical revisions - resolve conflicts | 10 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| L15-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 06-Jan-15 A | 07-Jan-15 A | |
| L07-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L08-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L09-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L10-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L09-7136 | Install Door and Hardware | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L10-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L11-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L12-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L15-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 06-Jan-15 A | 07-Jan-15 A | |
| L11-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 06-Jan-15 A | 12-Jan-15 A | |
| L03-8660 | GWB hang ceilings at Pool | 3 | 0 | 06-Jan-15 A | 04-Feb-15 A | |
| L1K-6011 | Complete HVAC RI @ ceilings | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L1K-6013 | Complete electrical rough-in @ ceilings & inspection | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L1K-6015 | Complete fire sprinkler RI @ ceilings | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L12-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L14-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L15-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |

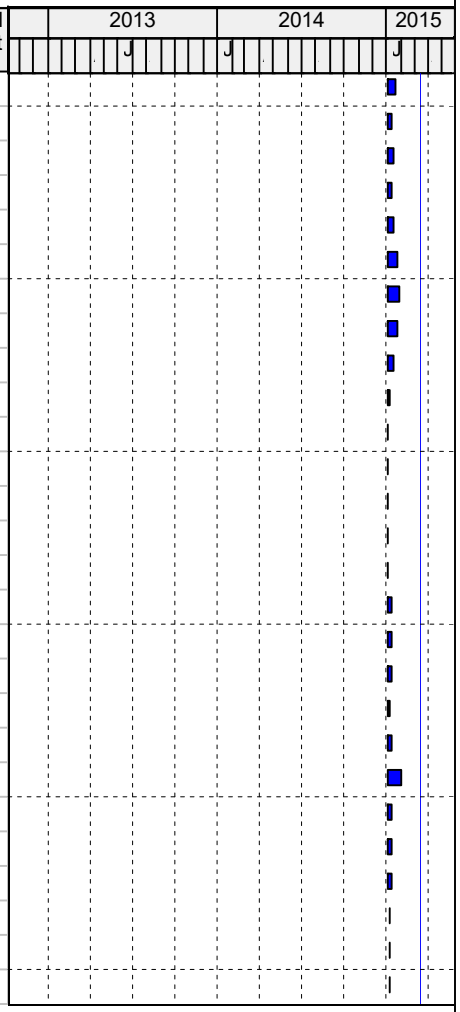



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L15-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 07-Jan-15 A | 20-Jan-15 A | |
| L12-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 07-Jan-15 A | 13-Jan-15 A | |
| CO-7242 | Cx - Heat Pump Start-Up - Levels 5 & 6 | 5 | 0 | 07-Jan-15 A | 09-Jan-15 A | |
| CO-7252 | Cx - Start-Up - FSD & SD Operation Verification | 10 | 0 | 07-Jan-15 A | 22-Jan-15 A | |
| MPP-1026 | Complete Elevation 7/8 (east elevation) | 5 | 0 | 07-Jan-15 A | 16-Feb-15 A | |
| ASI61 | ASI No. 61 - VHP-1 Ductwork Change at Elevator 5 L | 0 | 0 | 07-Jan-15 A | | |
| I-5056 | RFI 832.1 - South Elevation Emergency Exit with Sid | 1 | 0 | 07-Jan-15 A | 14-Jan-15 A | |
| LL1-6014Ib2 | L1 bar redesign - GWB hang, tape, finish (including ir | 12 | 0 | 08-Jan-15 A | 30-Jan-15 A | |
| SW-2310 | Zone 3 - Install irrigation sleeves | 2 | 0 | 08-Jan-15 A | 08-Jan-15 A | |
| I-1638 | Manlift finishes - ceiling grid | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| L03-8662 | GWB tape & finish walls & ceilings at Pool | 7 | 0 | 08-Jan-15 A | 25-Feb-15 A | |
| MPT-1072 | Tower Sign, West (El, 52) | 5 | 2 | 08-Jan-15 A | 17-Mar-15 | 29 |
| L1L-8220 | Complete fire sprinkler RI @ ceilings | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| L1L-8270 | Complete HVAC RI @ ceilings | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| SW-2224 | Zone 2 - Adjust Comcast vault lids | 2 | 0 | 08-Jan-15 A | 08-Jan-15 A | |
| I-1212 | Resolve stud/duct conflict at east wall | 5 | 0 | 08-Jan-15 A | 14-Jan-15 A | |
| L04-8218 | Install base at corridors (& approve mockup) | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| GB410-100 | Complete GWB - Levels 4-10 | 5 | 0 | 08-Jan-15 A | 14-Jan-15 A | |
| LL1-6014Ib4 | L1 bar redesign - complete reframing | 5 | 0 | 08-Jan-15 A | 15-Jan-15 A | |
| I-5306 | Heat Pump Revision - complete reframing | 5 | 0 | 08-Jan-15 A | 19-Jan-15 A | |
| ASI63 | ASI No. 63 - Mech (Rev. 20), Plumbing (Rev. 18) and | 0 | 0 | 09-Jan-15 A | | |
| L15-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L16-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8121 | Install Bathroom "Barn Doors" | 3 | 2 | 12-Jan-15 A | 19-Mar-15 | 17 |
| L04-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |

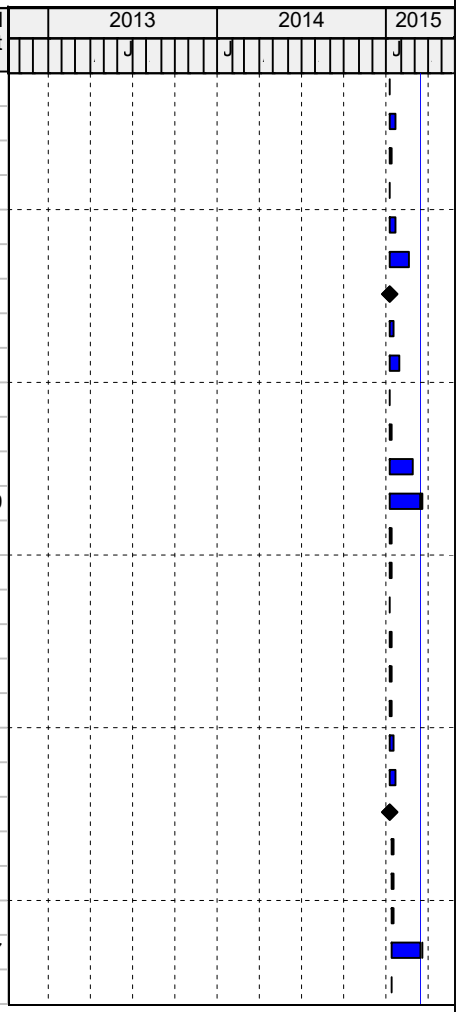



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L06-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L07-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L08-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L09-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L10-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L11-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L12-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L14-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L15-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L11-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L14-7136 | Install doors & hardware | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L14-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L15-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L15-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L14-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L11-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L03-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 12-Jan-15 A | 19-Jan-15 A | |
| CO-7244 | Cx - Heat Pump Start-Up - Levels 7 & 8 | 5 | 0 | 12-Jan-15 A | 14-Jan-15 A | |
| MPT-1068 | Tower Sign, North (El. 51) | 5 | 0 | 12-Jan-15 A | 10-Mar-15 A | |
| L03-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L11-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L14-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L15-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |

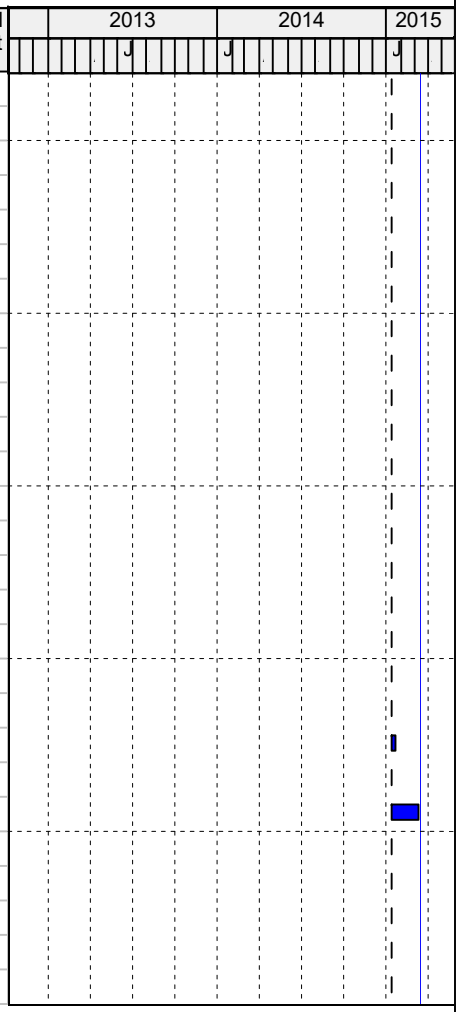



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8144 | GWB hang at Locker Rooms | 2 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| SW-2326 | Zone 3 - Install j-boxes | 3 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| I-5800 | Mechanical correction notice - interference with light t | 10 | 0 | 12-Jan-15 A | 13-Feb-15 A | |
| I-5602 | Frame FCC ceiling | 2 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| CO-7166 | Replace exhaust fitting | 10 | 0 | 12-Jan-15 A | 28-Jan-15 A | |
| MPP-1034 | Deliver Elevation 48 corner panels | 25 | 0 | 12-Jan-15 A | 27-Feb-15 A | |
| MPP-1042 | Deliver Elevation 32 corner panels | 25 | 0 | 12-Jan-15 A | 02-Feb-15 A | |
| MPP-1066 | Deliver Elevation 33/34 corner panels | 25 | 0 | 12-Jan-15 A | 27-Feb-15 A | |
| MPP-1068 | Deliver Elevation 32 spandrel panel head/sill flashings | 25 | 0 | 12-Jan-15 A | 13-Feb-15 A | |
| MPP-1070 | Deliver Elevation 44 spandrel panel head/sill flashings | 25 | 0 | 12-Jan-15 A | 13-Feb-15 A | |
| MPP-1072 | Deliver remaining Elevation 4 panels | 25 | 0 | 12-Jan-15 A | 06-Feb-15 A | |
| MPP-1074 | Deliver remaining Elevation 7 panels | 25 | 0 | 12-Jan-15 A | 06-Feb-15 A | |
| MPP-1076 | Deliver Pool cornice panels | 25 | 1 | 12-Jan-15 A | 16-Mar-15 | 18 |
| ASI64 | ASI No. 64 - Updated Public Space Carpet Specificat | 0 | 0 | 12-Jan-15 A | | |
| L15-7136 | Install doors & hardware | 1 | 0 | 13-Jan-15 A | 16-Feb-15 A | |
| L03-8664 | Paint, prime & first coat finish at Pool | 3 | 1 | 13-Jan-15 A | 16-Mar-15 | 18 |
| MPP-1022 | (A) Complete Elevation 40 (pool south elevation, L3-L | 5 | 0 | 13-Jan-15 A | 20-Jan-15 A | |
| L05-8226 | Install base at corridors | 1 | 0 | 13-Jan-15 A | 13-Jan-15 A | |
| L16-8138 | Bathrooms - Install toilet accessories | 2 | 0 | 14-Jan-15 A | 15-Jan-15 A | |
| L14-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| CO-7246 | Cx - Heat Pump Start-Up - Levels 9 & 10 | 5 | 0 | 14-Jan-15 A | 16-Jan-15 A | |
| I-5604 | GWB hang, tape & finish FCC ceiling | 5 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| I-5076 | RFI 860.1 - Southeast Elevation Conflict | 1 | 1 | 14-Jan-15 A | 16-Mar-15 | 28 |
| I-5078 | RFI 884 - Pedestrian Light Pole Base and Drain Conf | 1 | 0 | 14-Jan-15 A | 28-Jan-15 A | |
| L14-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 15-Jan-15 A | 16-Jan-15 A | |
| L16-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 15-Jan-15 A | 21-Jan-15 A | |
| SW-2126 | Zone 1 - Remove temporary transformer | 5 | 0 | 15-Jan-15 A | 28-Jan-15 A | |

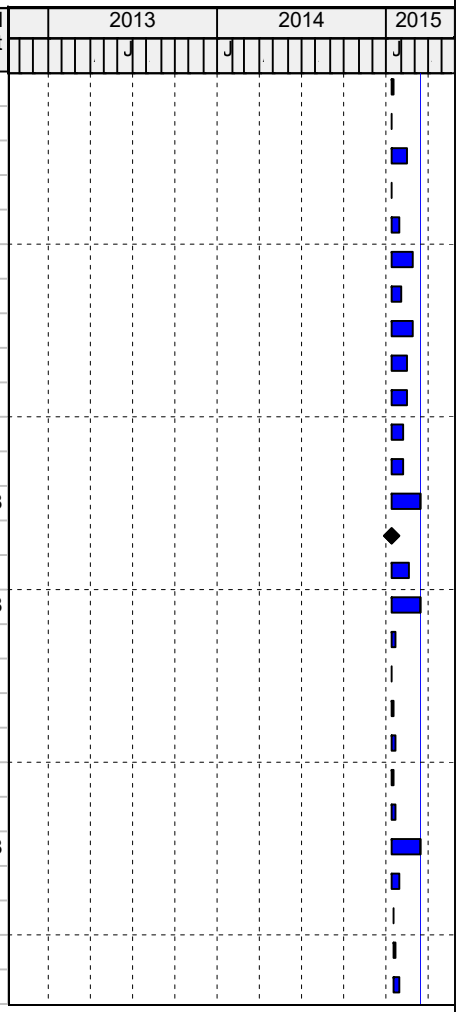



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-5112 | Bar radius ceiling - complete framing | 5 | 0 | 15-Jan-15 A | 20-Jan-15 A | |
| I-5080 | RFI 889 - Site Channelization Plan | 1 | 1 | 15-Jan-15 A | 16-Mar-15 | 36 |
| L07-8226 | Install base at corridors | 1 | 0 | 16-Jan-15 A | 16-Jan-15 A | |
| I-5060 | RFI 834.1 - NE Retaining Wall Design Clarifications - ( | 1 | 0 | 16-Jan-15 A | 02-Feb-15 A | |
| L16-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| CO-7248 | Cx - Heat Pump Start-Up - Levels 11 & 12 | 5 | 0 | 19-Jan-15 A | 21-Jan-15 A | |
| CO-7254 | Cx - Start-Up - MUA AAON (8) | 5 | 0 | 19-Jan-15 A | 20-Feb-15 A | |
| SW-2020 | Porte Cochere - EIFS at ceiling | 7 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L02-8146 | GWB tape & finish at Locker Rooms | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L1K-8138 | Complete GWB hang & tape | 9 | 0 | 19-Jan-15 A | 06-Feb-15 A | |
| L1L-8252 | Complete electrical/fire alarm rough-in @ ceilings | 3 | 0 | 19-Jan-15 A | 26-Jan-15 A | |
| LL1-8122 | Paint corridors | 6 | 0 | 19-Jan-15 A | 21-Jan-15 A | |
| L1B-6027 | Framing, ceiling at East Ballroom | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L09-8226 | Install base at corridors | 1 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| GB410-102 | Complete painting - Levels 4-10 | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL1-Z2-8110 | Paint, prime & first coat finish at Meeting Rooms | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| I-5122 | Dining feature wall - complete framing | 3 | 0 | 19-Jan-15 A | 21-Jan-15 A | |
| I-5162 | ASI 63 electrical revisions - demo existing | 1 | 0 | 19-Jan-15 A | 19-Jan-15 A | |
| L1B-8170 | Complete cover inspections | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L17-8138 | Bathrooms - Install toilet accessories | 2 | 1 | 20-Jan-15 A | 25-Mar-15 | 15 |
| MPP-1014 | Caulking - Elevation 1/2/A/B/C/23/24/25 (west elevati | 9 | 0 | 20-Jan-15 A | 30-Jan-15 A | |
| CO-7232 | Cx - TAB - CW Pump Totalization | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| L03-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| LL1-8202 | HVAC trim at ceiling | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| LL1-8206 | Lighting & electrical trim | 4 | 0 | 20-Jan-15 A | 28-Jan-15 A | |
| LL1-8208 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| LL1-Z2-8138 | Paint corridors | 3 | 0 | 20-Jan-15 A | 04-Feb-15 A | |

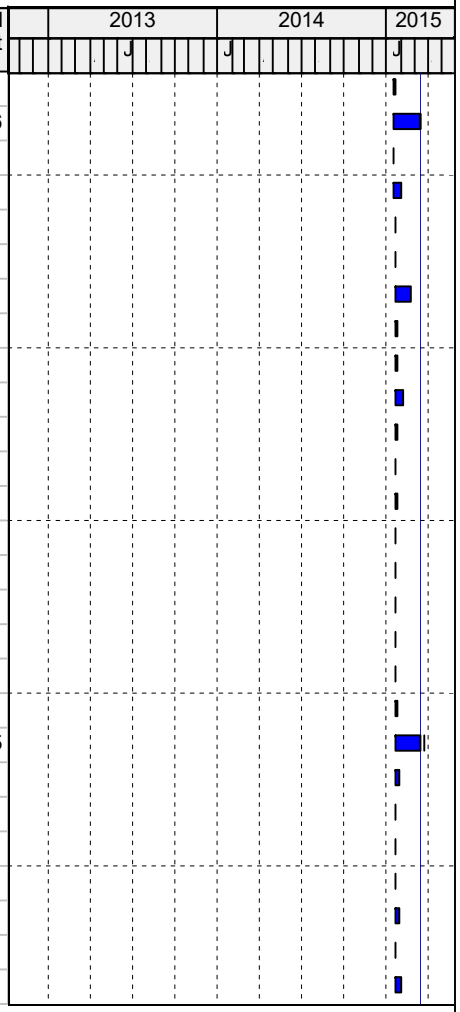



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8226 | Install base at corridors | 1 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| GB410-106 | Complete flooring - Levels 4-10 | 3 | 0 | 20-Jan-15 A | 26-Jan-15 A | |
| L04-8422 | Floor prep | 1 | 0 | 20-Jan-15 A | 02-Feb-15 A | |
| I-5606 | Paint FCC ceiling | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| I-5104 | Bar lighting layout - complete elecrical rough-in | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| I-5164 | ASI 63 electrical revisions - revise electrical | 3 | 0 | 20-Jan-15 A | 02-Feb-15 A | |
| L16-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| CO-7234 | Cx - TAB - CW Water Balancing | 10 | 0 | 21-Jan-15 A | 06-Mar-15 A | |
| L15-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L14-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L12-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L11-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L16-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| CO-7250 | Cx - Heat Pump Start-Up - Levels 14 & 15 | 5 | 0 | 21-Jan-15 A | 23-Jan-15 A | |
| L16-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| I-5304 | Heat Pump Revision - rework GWB | 9 | 0 | 21-Jan-15 A | 30-Jan-15 A | |
| L03-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L04-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L05-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L06-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L07-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L08-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L09-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L11-8226 | Install base at corridors | 1 | 0 | 21-Jan-15 A | 22-Jan-15 A | |
| L05-8422 | Floor prep | 1 | 0 | 21-Jan-15 A | 02-Feb-15 A | |
| ASI65 | ASI No. 65 - Framing Revisions at Foyer 101 | 0 | 0 | 21-Jan-15 A | | |
| L07-7134 | Flooring - VCT | 1 | 0 | 22-Jan-15 A | 22-Jan-15 A | |

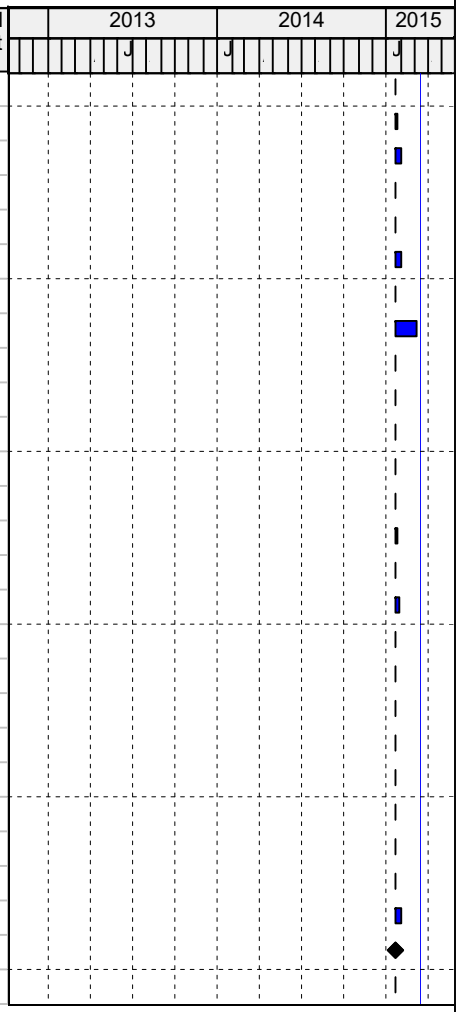



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 22-Jan-15 A | 27-Jan-15 A | |
| LL1-8210 | Fire sprinkler trim | 1 | 0 | 22-Jan-15 A | 22-Jan-15 A | |
| L12-8226 | Install base at corridors | 1 | 0 | 22-Jan-15 A | 23-Jan-15 A | |
| L05-7134 | Flooring - VCT | 1 | 0 | 23-Jan-15 A | 23-Jan-15 A | |
| MPP-1016 | Caulking - Elevation 7/8 (east elevation) | 8 | 0 | 23-Jan-15 A | 24-Feb-15 A | |
| LL1-Z2-8120 | GWB hang, tape & finish ceiling clouds at Jr. Ballroon | 7 | 0 | 23-Jan-15 A | 17-Feb-15 A | |
| LL1-Z3-8148 | Paint Restrooms | 3 | 0 | 23-Jan-15 A | 26-Jan-15 A | |
| MPT-1104 | (B) Install alcoves, east (Elev. 7/8) | 2 | 0 | 23-Jan-15 A | 09-Feb-15 A | |
| L06-8422 | Floor prep | 1 | 0 | 23-Jan-15 A | 23-Jan-15 A | |
| L17-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L06-7134 | Flooring - VCT | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| CO-7216 | Cx - Start-Up Fluid Cooler (power, pre-start & start) | 3 | 0 | 26-Jan-15 A | 28-Jan-15 A | |
| L16-8140 | Install window sills | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| L04-8224 | HVAC grilles & registers at corridors | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| MPT-1058 | Elevation 32 hat channel (south elevation, east of ma | 3 | 0 | 26-Jan-15 A | 17-Feb-15 A | |
| MPT-1090 | Caulking - Elevation 40 (pool south elevation, L3-L17 | 9 | 0 | 26-Jan-15 A | 05-Feb-15 A | |
| LL1-8123 | Floor prep | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| SW-2052 | Zone 4 - Waterproof NW planter walls | 4 | 0 | 26-Jan-15 A | 29-Jan-15 A | |
| L1L-8290 | GWB, top rock | 3 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L10-8131 | Bathrooms - Install access panels | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| L14-8226 | Install base at corridors | 1 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| I-5372 | (S) Elevation 32, complete insulation | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| GB1117-100 | Complete GWB - Levels 3, 11-16 | 7 | 0 | 26-Jan-15 A | 30-Jan-15 A | |
| SW-2322 | Zone 3 - FRP landscape curb at exit door | 5 | 0 | 26-Jan-15 A | 30-Jan-15 A | |
| I-6010 | RFI 901 - Pool topping slab issue (Owner procure floc | 10 | 10 | 26-Jan-15 A | 27-Mar-15 | 0 |
| L03-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L16-7034 | Install doors & hardware (x42) | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |

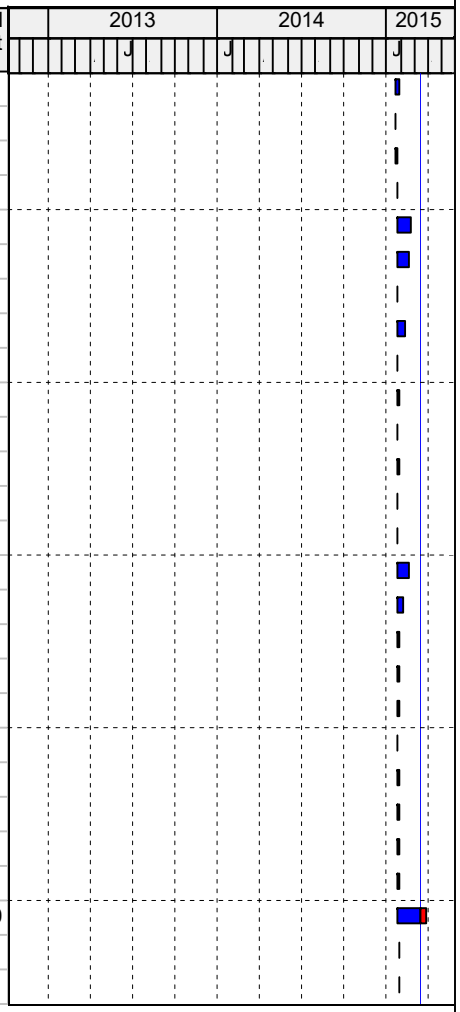



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7034 | Install doors & hardware (x42) | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L08-7134 | Flooring - VCT | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L16-7138 | Electrical trim & finish | 1 | 0 | 27-Jan-15 A | 18-Feb-15 A | |
| L17-7136 | Install doors & hardware | 1 | 0 | 27-Jan-15 A | 17-Feb-15 A | |
| I-1640 | Manlift finishes - Install window sills | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L03-8668 | Remove scaffolding at pool pit | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L17-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L11-8131 | Bathrooms - Install access panels | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L15-8226 | Install base at corridors | 1 | 0 | 27-Jan-15 A | 28-Jan-15 A | |
| MPP-1052 | (B) Elevation 3 (south elevation, west of manlift, L1-L: | 5 | 0 | 27-Jan-15 A | 30-Jan-15 A | |
| GB410-108 | Complete base - Levels 4-10 | 4 | 0 | 27-Jan-15 A | 30-Jan-15 A | |
| L08-8422 | Floor prep | 1 | 0 | 27-Jan-15 A | 28-Jan-15 A | |
| I-5132 | Bar plumbing relocation - relocate waste line | 3 | 0 | 27-Jan-15 A | 29-Jan-15 A | |
| I-5152 | Sprinkler pipe furring - install framing around pipe | 2 | 0 | 27-Jan-15 A | 28-Jan-15 A | |
| L09-7134 | Flooring - VCT | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L17-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L17-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| EL-6042 | Elev 6 - Install EMR heat pump | 6 | 0 | 28-Jan-15 A | 25-Feb-15 A | |
| MPT-1056 | Complete Elevation 31 (above L12 terrace, west elev | 3 | 0 | 28-Jan-15 A | 13-Feb-15 A | |
| L1L-8256 | GWB hang walls | 3 | 0 | 28-Jan-15 A | 05-Feb-15 A | |
| SW-2230 | Zone 2 - Repair sidewalk north of 3rd Ave | 5 | 0 | 28-Jan-15 A | 30-Jan-15 A | |
| L12-8131 | Bathrooms - Install access panels | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L08-8226 | Install base at corridors | 1 | 0 | 28-Jan-15 A | 30-Jan-15 A | |
| L16-8226 | Install base at corridors | 1 | 0 | 28-Jan-15 A | 29-Jan-15 A | |
| I-5373 | (S) Elevation 32, install sign backing | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L07-8422 | Floor prep | 1 | 0 | 28-Jan-15 A | 03-Feb-15 A | |
| I-6000 | Resolve cloud framing engineering issue | 5 | 0 | 28-Jan-15 A | 03-Feb-15 A | |

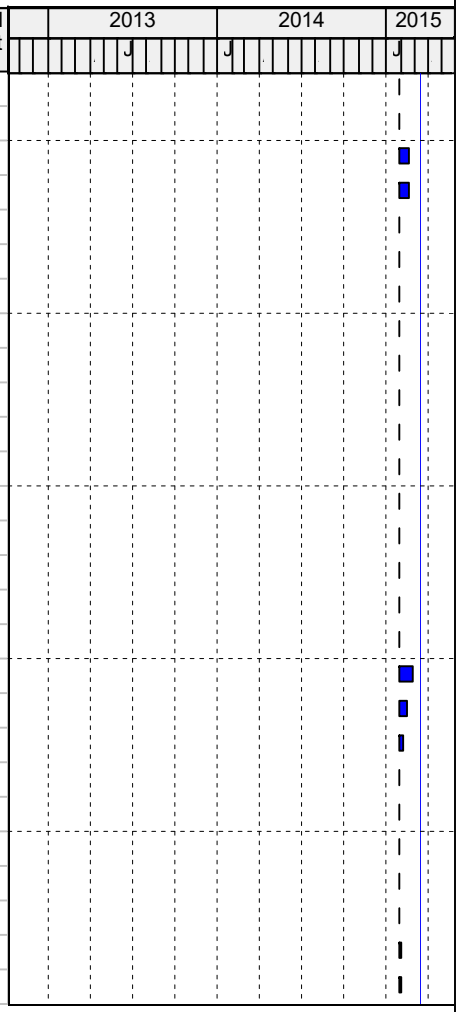



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7134 | Flooring - VCT | 1 | 0 | 29-Jan-15 A | 29-Jan-15 A | |
| L1L-8226 | GWB hang ceilings & complete walls | 3 | 0 | 29-Jan-15 A | 23-Feb-15 A | |
| L1L-8248 | Complete electrical/fire alarm rough-in @ ceilings | 3 | 0 | 29-Jan-15 A | 02-Feb-15 A | |
| L1L-8250 | Complete HVAC RI @ ceilings | 5 | 0 | 29-Jan-15 A | 04-Feb-15 A | |
| L03-8218 | Install base at corridors | 1 | 0 | 29-Jan-15 A | 30-Jan-15 A | |
| MPP-1062 | (C) Install level 3 cornice metal (Porte Cochere) | 2 | 0 | 29-Jan-15 A | 04-Feb-15 A | |
| EL-6040 | Elev 6 - Install machine room controller equipment/hy | 3 | 0 | 30-Jan-15 A | 24-Feb-15 A | |
| EL-6054 | Elev 6 - Install EMR doors, hardware & labeling | 2 | 0 | 30-Jan-15 A | 23-Feb-15 A | |
| LL1-8160 | Flooring - carpet | 10 | 0 | 30-Jan-15 A | 18-Feb-15 A | |
| I-5472 | Reframe Laundry Room ceiling (per ceiling height RF | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5474 | Restore Laundry Room GWB (hang & tape) (per ceili | 5 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5476 | Repaint Laundry Room ceiling | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5478 | Demo existing Laundry Room ceiling | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5480 | Revise MEP above Laundry Room ceiling | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5134 | Bar plumbing relocation - adust framing | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5136 | Bar plumbing relocation - GWB hang, tape & finish [D | 7 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5138 | Bar plumbing relocation - paint [DELETED] | 2 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5142 | Damper at BPF #8 - mechanical revisions | 2 | 0 | 30-Jan-15 A | 02-Feb-15 A | |
| L04-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 02-Feb-15 A | 02-Feb-15 A | |
| L04-7134 | Flooring - VCT | 1 | 0 | 02-Feb-15 A | 02-Feb-15 A | |
| LL1-8124a | Install base | 10 | 0 | 02-Feb-15 A | 23-Feb-15 A | |
| CO-7218 | Cx - Heat Pump Start-Up - Levels 16 & 17 | 5 | 0 | 02-Feb-15 A | 04-Feb-15 A | |
| LL1-6014Id | L1 bar redesign - paint ceilings at Excercise & MR9 | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| EL-1236 | Elev 1&2 - Walsh/TKE pre-inspection | 6 | 0 | 02-Feb-15 A | 27-Feb-15 A | |
| MPT-1050 | (B) Install louvers, east | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| MPT-1070 | Tower Sign, East (El. 44) | 5 | 0 | 02-Feb-15 A | 10-Feb-15 A | |
| L1L-8272 | GWB hang ceilings | 3 | 0 | 02-Feb-15 A | 04-Feb-15 A | |

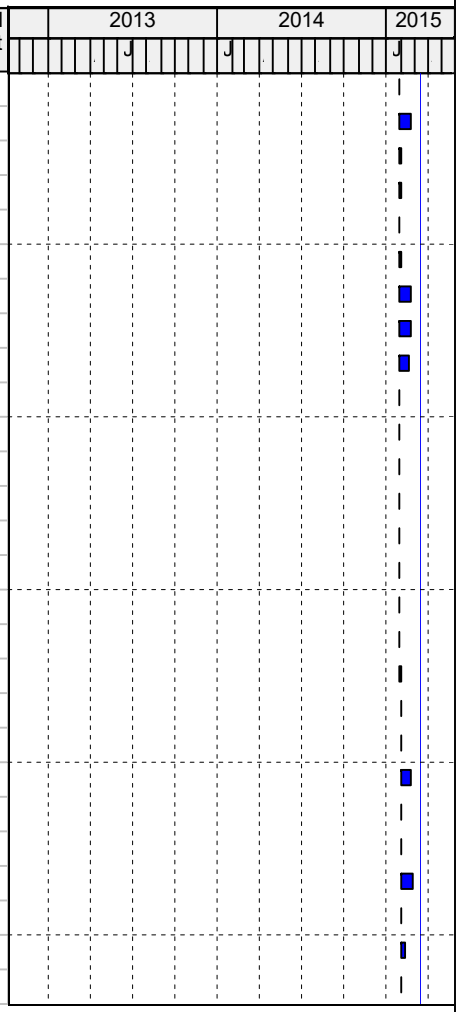



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2320 | Zone 3 - Pour ped pole base | 3 | 0 | 02-Feb-15 A | 05-Feb-15 A | |
| LL1-8156 | Install doors & hardware at corridors | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| L1B-6015 | HVAC drops at West Ballrooms | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L1B-6021 | Electrical drops at West Ballrooms | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L1B-6029 | HVAC drops at East Ballroom | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L1B-6031 | Electrical drops at East Ballroom | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L06-8226 | Install base at corridors | 1 | 0 | 02-Feb-15 A | 02-Feb-15 A | |
| GB410-104 | Complete vinyl wallcoverings - Levels 4-10 | 4 | 0 | 02-Feb-15 A | 17-Feb-15 A | |
| GB1117-102 | Complete painting - Levels 3, 11-16 | 3 | 0 | 02-Feb-15 A | 04-Feb-15 A | |
| SW-2234 | Zone 2 - FRP door curbs | 4 | 0 | 02-Feb-15 A | 05-Feb-15 A | |
| I-6950 | Resolve MEP/ceiling height conflicts | 1 | 0 | 02-Feb-15 A | 13-Mar-15 A | |
| L05-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L04-7138 | Electrical trim & finish | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L05-7138 | Electrical trim & finish | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L11-7134 | Flooring - VCT | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| SW-2022 | Zone 4 - Remove pedestrian protection on 110th Ave | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L1L-8246 | Complete fire sprinkler RI @ ceilings | 2 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| LL1-8184 | Install storefront at Exercise Room | 1 | 0 | 03-Feb-15 A | 02-Mar-15 A | |
| L12-8422 | Floor prep | 1 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| L14-8422 | Floor prep | 1 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| L15-8422 | Floor prep | 1 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| I-5144 | Damper at BPF #8 - framing revisions | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| I-5154 | Sprinkler pipe furring - GWB hang | 7 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| I-5166 | ASI 63 electrical revisions - insulation | 2 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| ASI62r1 | ASI No. 62 (Revised) - Civil Site Grading Revisions an | 0 | 0 | 03-Feb-15 A | | |
| L06-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 04-Feb-15 A | 04-Feb-15 A | |
| L12-7134 | Flooring - VCT | 1 | 0 | 04-Feb-15 A | 04-Feb-15 A | |

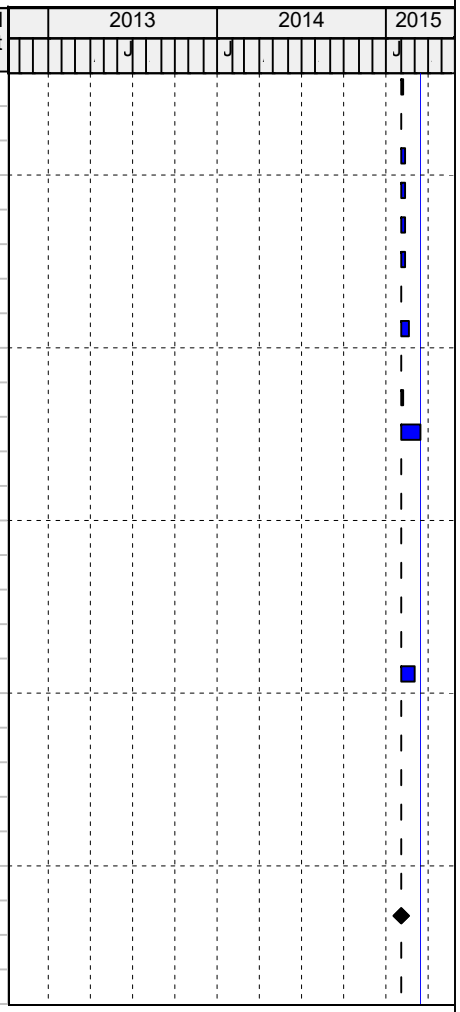



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8142 | Ceramic tile in restrooms | 7 | 0 | 04-Feb-15 A | 20-Feb-15 A | |
| L1K-8144 | Paint, prime & first coat finish | 3 | 0 | 04-Feb-15 A | 09-Mar-15 A | |
| LL1-Z2-8158 | Wall coverings - vinyl at Meeting Rooms | 2 | 0 | 04-Feb-15 A | 05-Feb-15 A | |
| L09-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 06-Feb-15 A | |
| L10-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 09-Feb-15 A | |
| L11-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 09-Feb-15 A | |
| L16-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 10-Feb-15 A | |
| I-5146 | Damper at BPF #8 - complete GWB hang | 1 | 0 | 04-Feb-15 A | 04-Feb-15 A | |
| I-5168 | ASI 63 electrical revisions - vapor barrier | 2 | 0 | 04-Feb-15 A | 05-Feb-15 A | |
| L07-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 05-Feb-15 A | 05-Feb-15 A | |
| L14-7134 | Flooring - VCT | 1 | 0 | 05-Feb-15 A | 05-Feb-15 A | |
| L1L-8102a | GWB tape & finish walls & ceilings (Dining & Lounge) | 7 | 0 | 05-Feb-15 A | 12-Feb-15 A | |
| LL1-8170 | Flooring - tile at elevator lobby | 3 | 0 | 05-Feb-15 A | 09-Feb-15 A | |
| LL1-8186 | Wall coverings - vinyl at corridors | 5 | 0 | 05-Feb-15 A | 19-Feb-15 A | |
| L1B-6023 | Fire sprinkler drops at West Ballrooms | 5 | 0 | 05-Feb-15 A | 09-Feb-15 A | |
| L1B-6033 | Fire sprinkler drops at East Ballroom | 5 | 0 | 05-Feb-15 A | 09-Feb-15 A | |
| GB1117-106 | Complete flooring - Levels 3, 11-16 | 4 | 0 | 05-Feb-15 A | 10-Feb-15 A | |
| I-6100 | Resolve lighting/access panel conflict | 5 | 0 | 05-Feb-15 A | 13-Feb-15 A | |
| GB1117-104 | Complete vinyl wallcoverings - Levels 3, 11-16 | 5 | 0 | 05-Feb-15 A | 11-Feb-15 A | |
| L08-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 06-Feb-15 A | 06-Feb-15 A | |
| L15-7134 | Flooring - VCT | 1 | 0 | 06-Feb-15 A | 06-Feb-15 A | |
| MPP-1054 | Caulking - Elevation 3 (south elevation, west of manli | 3 | 0 | 06-Feb-15 A | 10-Feb-15 A | |
| ASI66 | ASI No. 66 - MDP Electrical Drawings Revision 23A | 0 | 0 | 06-Feb-15 A | | |
| L03-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L04-8408 | Install base at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L05-8408 | Install base at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L06-8408 | Install base at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |

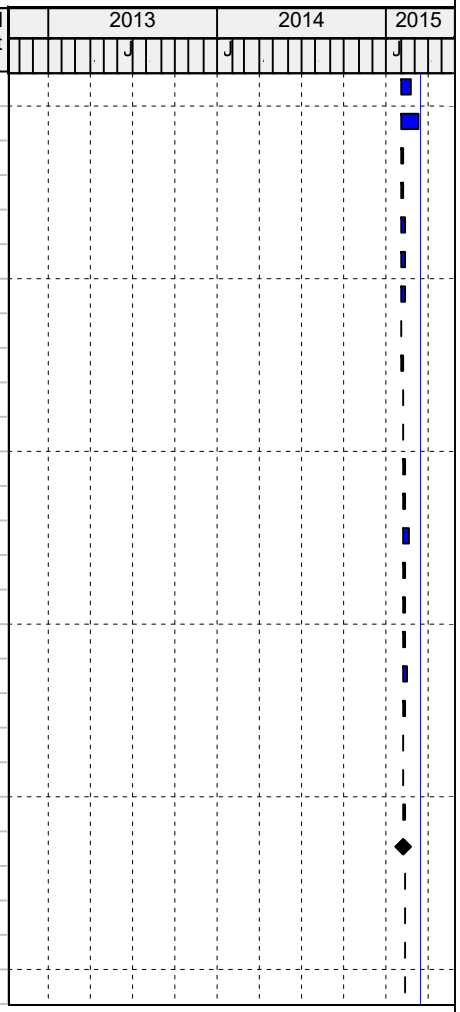



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L16-7134 | Flooring - VCT | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L1K-8102a | GWB hang ceilings at Public Restroom | 2 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| LL2-2094 | Install doors & hardware at Laundry | 2 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| SW-2032 | Zone 4 - Demo existing trees & hardscapes | 3 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| CO-7139 | Install remaining devices & prep devices for testing - | 7 | 0 | 09-Feb-15 A | 03-Mar-15 A | |
| MPP-1024 | (B) Complete Elevation 4 (south elevation, east of tov | 2 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| L1L-8218 | Frame ceilings & inspection | 5 | 0 | 09-Feb-15 A | 12-Feb-15 A | |
| L1K-8136 | Ceiling grid & inspection | 4 | 0 | 09-Feb-15 A | 11-Feb-15 A | |
| L1L-8274 | GWB tape & finish walls & ceilings | 7 | 0 | 09-Feb-15 A | 24-Feb-15 A | |
| L15-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L16-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L17-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L14-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| I-5170 | ASI 63 electrical revisions - GWB hang, tape & finish | 7 | 0 | 09-Feb-15 A | 17-Feb-15 A | |
| SW-2058 | Zone 4 - Demo existing curb at 110th | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| MPT-1114 | Cap metal - Porte Cochere | 3 | 0 | 09-Feb-15 A | 12-Feb-15 A | |
| I-5172 | Resolve Bar Area RFIs & complete revised work | 10 | 0 | 09-Feb-15 A | 04-Mar-15 A | |
| I-2960 | Lack of Stainless Steel Ceiling Closure Pieces (Shrou | 5 | 0 | 09-Feb-15 A | 13-Mar-15 A | |
| L07-8408 | Install base at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L08-8408 | Install base at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L09-8408 | Install base at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L10-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L11-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L17-7134 | Flooring - VCT | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L09-8224 | HVAC grilles & registers at corridors | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L08-8224 | HVAC grilles & registers at corridors | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |

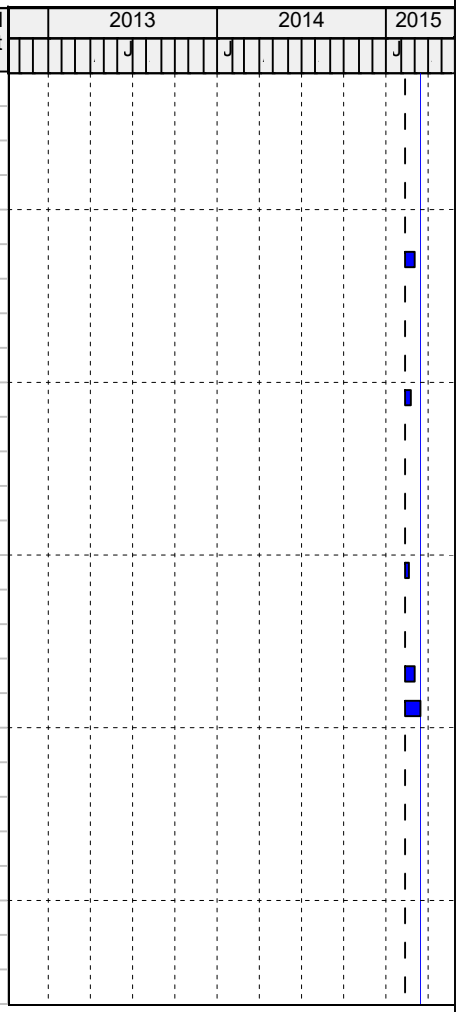



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8224 | HVAC grilles & registers at corridors | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| SW-2036 | Zone 4 - Grade for curb and gutter | 2 | 0 | 10-Feb-15 A | 11-Feb-15 A | |
| CO-7140 | Fire Alarm System Device Testing - Tower Levels 4 thr | 7 | 0 | 10-Feb-15 A | 05-Mar-15 A | |
| L17-8422 | Floor prep | 1 | 0 | 10-Feb-15 A | 11-Feb-15 A | |
| MPT-1116 | Cap metal - Pool high roof | 3 | 0 | 10-Feb-15 A | 12-Feb-15 A | |
| ASI67 | ASI No. 67 - Meeting Room Door Hardware Revisions | 0 | 0 | 10-Feb-15 A | | |
| L10-8408 | Install base at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L11-8408 | Install base at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L12-8408 | Install base at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L12-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L14-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L03-7134 | Flooring - VCT | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| MPT-1018a | Install hi-roof cornice metal | 8 | 3 | 11-Feb-15 A | 18-Mar-15 | 33 |
| SW-2038 | Zone 4 - FRP curb & gutter | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| SW-2046 | Zone 4 - Install conduit | 2 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L1K-8152 | Install doors & hardware | 3 | 0 | 11-Feb-15 A | 17-Feb-15 A | |
| L1L-8228 | GWB tape & finish | 7 | 0 | 11-Feb-15 A | 03-Mar-15 A | |
| SW-2054 | Zone 4 - Install flag pole bases | 3 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| L17-8226 | Install base at corridors | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| MPP-1058 | (B) Install podium cornice, south/east | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| L03-8422 | Floor prep | 1 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| MPT-1108 | Cap metal - complete at tower | 5 | 0 | 11-Feb-15 A | 13-Feb-15 A | |
| MPT-1112 | Cap metal - complete at Ballroom roof | 3 | 0 | 11-Feb-15 A | 13-Feb-15 A | |
| L14-8408 | Install base at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L15-8408 | Install base at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L15-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L16-8408 | Install base at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |

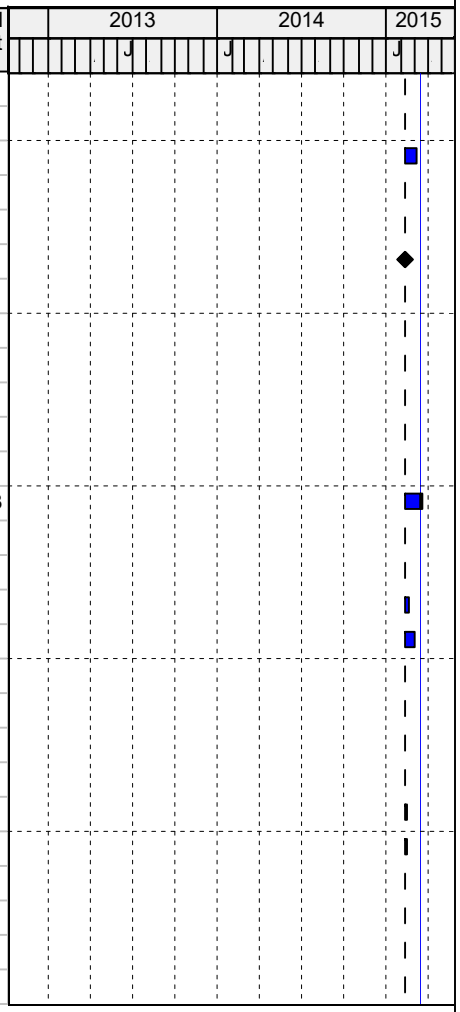



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L06-7138 | Electrical trim & finish | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L1K-8102b | GWB tape & finish at Restrooms | 7 | 0 | 12-Feb-15 A | 25-Feb-15 A | |
| LL1-8154 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 12-Feb-15 A | 20-Feb-15 A | |
| ASI68 | ASI No. 68 - MDP Mechanical Drawings Revision 21 | 0 | 0 | 12-Feb-15 A | | |
| LL1-Z3-FCC28 | Electrical trim & finish at FCC | 4 | 0 | 12-Feb-15 A | 16-Feb-15 A | |
| LL1-8182 | Install doors & hardware at Exercise Room | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| GB1117-108 | Complete base - Levels 3, 11-16 | 5 | 0 | 12-Feb-15 A | 18-Feb-15 A | |
| GB1117-110 | Complete countertops - Levels 3, 11-16 | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| GB1117-112 | Complete shower/tub surrounds - Levels 3, 11-16 | 3 | 0 | 12-Feb-15 A | 16-Feb-15 A | |
| L17-8408 | Install base at Elevator Lobby | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| L17-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| SW-2118 | Zone 1 - FRP sidewalk (NE corner) | 2 | 0 | 13-Feb-15 A | 13-Mar-15 A | |
| SW-2034 | Zone 4 - Install irrigation sleeves | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| SW-2060 | Zone 4 - Sawcut curb & gutter | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| ASI69 | ASI No. 69 - Architectural Level 1 Revised Ceiling Pla | 0 | 0 | 13-Feb-15 A | | |
| LL1-Z2-8142 | Wall coverings - vinyl at corridors | 3 | 0 | 16-Feb-15 A | 19-Feb-15 A | |
| I-6900 | Resolve Garage EF motor/VFD issue (including corre | 20 | 5 | 16-Feb-15 A | 20-Mar-15 | 32 |
| I-5066 | RFI 848.1 -Flagpole Lighting - South Light/Flagpole E | 1 | 1 | 16-Feb-15 A | 16-Mar-15 | 35 |
| L03-7136 | Install doors & hardware | 2 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| MPP-1012 | Caulking - Elevation 4 (south elevation, east of tower) | 6 | 0 | 16-Feb-15 A | 23-Feb-15 A | |
| L10-8224 | HVAC grilles & registers at corridors | 1 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| L06-8224 | HVAC grilles & registers at corridors | 1 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| L05-8224 | HVAC grilles & registers at corridors | 1 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| SW-2040 | Zone 4 - Fine grade for sidewalk and planter curb | 3 | 0 | 16-Feb-15 A | 17-Feb-15 A | |
| MPP-1036 | Podium Signs, East | 5 | 0 | 16-Feb-15 A | 18-Feb-15 A | |
| L1K-8150 | HVAC drops/trim at ceiling | 2 | 0 | 16-Feb-15 A | 17-Feb-15 A | |

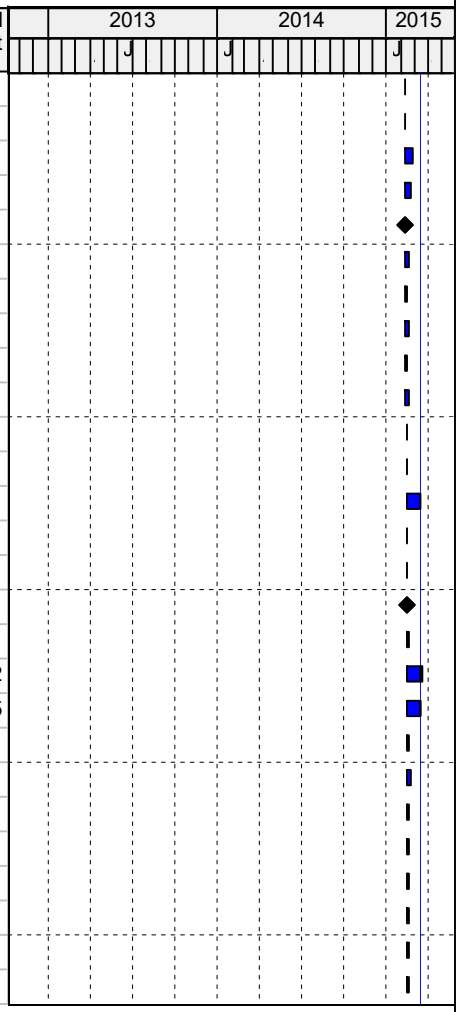



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-8146 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 16-Feb-15 A | 23-Feb-15 A | |
| LL1-8172 | Ceiling grid & inspection at Exercise Room (additional | 6 | 0 | 16-Feb-15 A | 23-Feb-15 A | |
| L1K-8162 | Complete wallcoverings (FRP) | 2 | 0 | 16-Feb-15 A | 17-Feb-15 A | |
| L1B-6011 | GWB, hang ceiling at West Ballrooms | 4 | 0 | 16-Feb-15 A | 18-Feb-15 A | |
| L1B-8138 | GWB hang, tape & finish ceilings at corridors (comple | 11 | 7 | 16-Feb-15 A | 01-Apr-15 | 2 |
| LL1-8176 | HVAC drops/trim to grid | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L03-8408 | Install base at Elevator Lobby | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L03-7034 | Install doors & hardware (x42) | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L03-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L07-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L08-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L09-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L10-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L11-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L12-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L16-7136 | Install doors & hardware | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| LL2-2062 | Ceiling grid at Laundry | 4 | 1 | 17-Feb-15 A | 18-Mar-15 | 19 |
| L15-8224 | HVAC grilles & registers at corridors | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L14-8224 | HVAC grilles & registers at corridors | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| CO-7258 | Cx - Start-Up - KMUA Trane (2) | 2 | 0 | 17-Feb-15 A | 20-Feb-15 A | |
| SW-2044 | Zone 4 - FRP sidewalk (SW corner remaining) | 3 | 3 | 17-Feb-15 A | 01-Apr-15 | 21 |
| LL1-Z3-FCC30 | Data/phone trim/finish at FCC | 4 | 0 | 17-Feb-15 A | 19-Feb-15 A | |
| LL1-Z3-6036 | GWB hang, tape & finish ceiling at Food Prep (Dry St | 5 | 0 | 17-Feb-15 A | 02-Mar-15 A | |
| MPT-1092 | Caulking - Elevation 31 (above L12 terrace, west elev | 4 | 0 | 17-Feb-15 A | 20-Feb-15 A | |
| MPT-1098 | Caulking - Elevation 30 (south elevation, west of man | 6 | 1 | 17-Feb-15 A | 17-Mar-15 | 34 |
| LL1-6014Id2 | L1 bar redesign - install wall coverings at MR9 | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L1K-8146 | Fire sprinkler drops/trim at ceiling | 1 | 0 | 17-Feb-15 A | 10-Mar-15 A | |

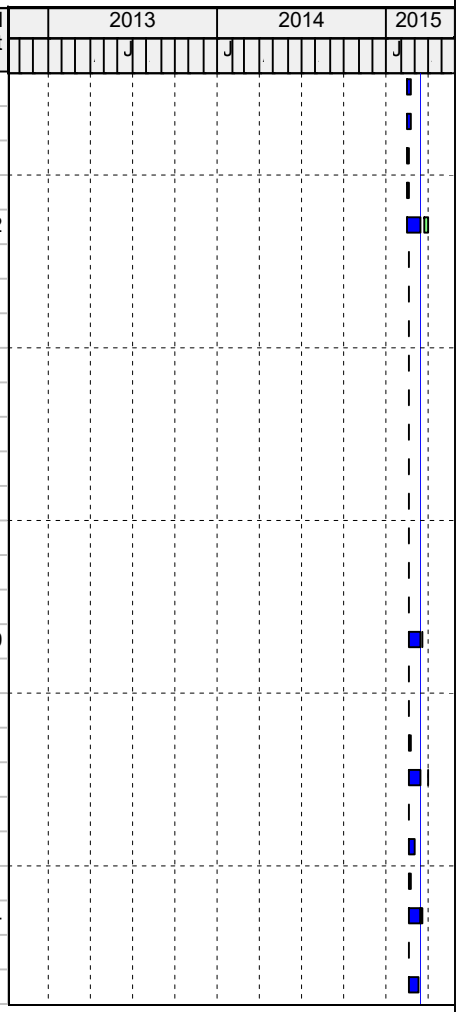



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8148 | Lighting & electrical trim at ceiling | 2 | 0 | 17-Feb-15 A | 10-Mar-15 A | |
| GB1117-114 | Complete plumbing fixture installation - Levels 3, 11-1 | 4 | 0 | 17-Feb-15 A | 20-Feb-15 A | |
| L1K-8164 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 17-Feb-15 A | 10-Mar-15 A | |
| MPT-1062 | Elevation 32 metal panels (south elevation, east of m | 8 | 1 | 18-Feb-15 A | 16-Mar-15 | 14 |
| L14-7138 | Electrical trim & finish | 1 | 0 | 18-Feb-15 A | 18-Feb-15 A | |
| L15-7138 | Electrical trim & finish | 1 | 0 | 18-Feb-15 A | 18-Feb-15 A | |
| L17-7138 | Electrical trim & finish | 1 | 0 | 18-Feb-15 A | 18-Feb-15 A | |
| CO-7262 | Cx - Start-Up - Electric Unit Heaters | 3 | 1 | 18-Feb-15 A | 16-Mar-15 | 36 |
| LL1-8174 | Wall coverings - vinyl at Exercise Room | 2 | 0 | 18-Feb-15 A | 19-Feb-15 A | |
| L1B-6017 | GWB, hang ceiling at East Ballrooms | 4 | 0 | 18-Feb-15 A | 20-Feb-15 A | |
| SW-2062 | Zone 4 - Patch curb & gutter | 2 | 0 | 18-Feb-15 A | 19-Feb-15 A | |
| CO-7256 | Cx - Start-Up - Elevator Machine Room Ductless Split | 1 | 0 | 19-Feb-15 A | 19-Feb-15 A | |
| LL1-8178 | Lighting & electrical drops to grid | 2 | 0 | 19-Feb-15 A | 20-Feb-15 A | |
| LL1-8180 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 19-Feb-15 A | 20-Feb-15 A | |
| GB410-110 | Complete countertops - Levels 4-10 | 1 | 0 | 19-Feb-15 A | 19-Feb-15 A | |
| GB410-112 | Complete shower/tub surrounds - Levels 4-10 | 1 | 0 | 19-Feb-15 A | 19-Feb-15 A | |
| GB410-118 | Complete barn doors - Levels 4-10 | 1 | 0 | 19-Feb-15 A | 19-Feb-15 A | |
| GB1117-118 | Complete barn doors - Levels 3, 11-16 | 2 | 0 | 19-Feb-15 A | 20-Feb-15 A | |
| LL1-Z2-8160a | Flooring - carpet at Meeting Rooms | 2 | 0 | 19-Feb-15 A | 23-Feb-15 A | |
| LL2-2098 | HVAC drops to grid at Laundry | 2 | 0 | 20-Feb-15 A | 04-Mar-15 A | |
| LL2-2088 | Lighting & electrical drops to grid at Laundry | 2 | 0 | 20-Feb-15 A | 09-Mar-15 A | |
| L1K-8123 | Floor prep | 2 | 0 | 20-Feb-15 A | 23-Feb-15 A | |
| LL1-8158 | Floor prep at corridors | 2 | 0 | 20-Feb-15 A | 23-Feb-15 A | |
| L1B-8102a | GWB, tape & finish ceiling at West Ballroom | 7 | 0 | 20-Feb-15 A | 02-Mar-15 A | |
| GB410-114 | Complete plumbing fixture installation - Levels 4-10 | 3 | 0 | 20-Feb-15 A | 24-Feb-15 A | |
| LL2-2106 | Floor prep | 1 | 0 | 20-Feb-15 A | 20-Feb-15 A | |
| LL2-2086 | Flooring - epoxy remainder of floor (including prep) | 6 | 0 | 21-Feb-15 A | 26-Feb-15 A | |

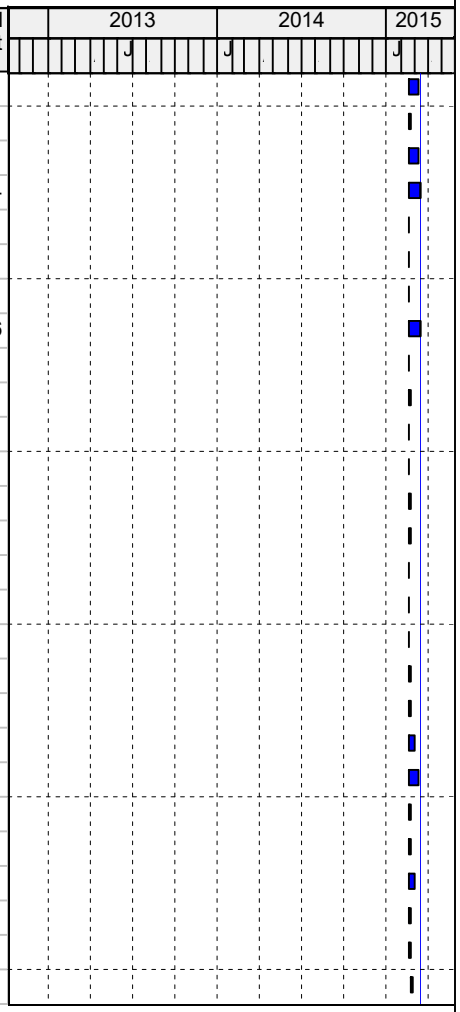



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPT-1102 | Elevation 32 spandrel panels (south elevation, east o | 2 | 1 | 21-Feb-15 A | 16-Mar-15 | 14 |
| LL2-2104 | Flooring - epoxy at equipment alcoves | 5 | 0 | 21-Feb-15 A | 26-Feb-15 A | |
| LL1-Z3-8164 | Field measure & fabricate countertops | 15 | 10 | 21-Feb-15 A | 27-Mar-15 | 8 |
| LL1-8116f | Fabricate & deliver countertops | 10 | 10 | 21-Feb-15 A | 27-Mar-15 | 12 |
| LL1-Z2-8118a | Install decorative light fixtures | 3 | 0 | 23-Feb-15 A | 03-Mar-15 A | |
| LL1-Z2-8124a | Install base | 10 | 0 | 23-Feb-15 A | 27-Feb-15 A | |
| CO-7400 | Cx - 3rd Party Cx of Mechanical, Plumbing, Electrical | 40 | 25 | 23-Feb-15 A | 17-Apr-15 | 16 |
| LL1-Z3-8144 | Install toilets at Restrooms | 4 | 0 | 23-Feb-15 A | 27-Feb-15 A | |
| LL1-8166 | Install base at corridors | 5 | 0 | 23-Feb-15 A | 27-Feb-15 A | |
| LL1-Z2-8122 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 23-Feb-15 A | 09-Mar-15 A | |
| GB1117-116 | Complete shower doors - Levels 3, 11-16 | 2 | 0 | 23-Feb-15 A | 24-Feb-15 A | |
| L17-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| L16-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| L12-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| L11-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| L03-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| MPT-1100 | Install spandrel, east (Elevation 44) | 2 | 0 | 24-Feb-15 A | 26-Feb-15 A | |
| SW-2064 | Porte Cochere - Fill and grade Porte Cochere drive | 3 | 0 | 24-Feb-15 A | 06-Mar-15 A | |
| L1BOH2-8104 | Paint, prime | 2 | 1 | 24-Feb-15 A | 16-Mar-15 | 7 |
| L1K-8124a | Flooring - epoxy - east end | 5 | 0 | 24-Feb-15 A | 26-Feb-15 A | |
| LL2-8148 | Fire sprinkler drops to grid | 1 | 0 | 24-Feb-15 A | 09-Mar-15 A | |
| LL1-8162 | Flooring - carpet at corridors | 5 | 0 | 24-Feb-15 A | 02-Mar-15 A | |
| LL1-Z2-8128 | HVAC trim at ceiling | 1 | 0 | 24-Feb-15 A | 03-Mar-15 A | |
| LL1-Z2-8130 | Fire sprinkler trim | 1 | 0 | 24-Feb-15 A | 04-Mar-15 A | |
| MPT-1052 | Elevation 48/49 (north elevation, east of 51, L3-L17) | 3 | 0 | 25-Feb-15 A | 11-Mar-15 A | |
| CO-7100T | Cx - Start-Up - Life Safety Exhaust Fans and VFD's | 13 | 5 | 25-Feb-15 A | 20-Mar-15 | 19 |
| EL-6044 | Elev 6 - Electrical trim & finish | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |

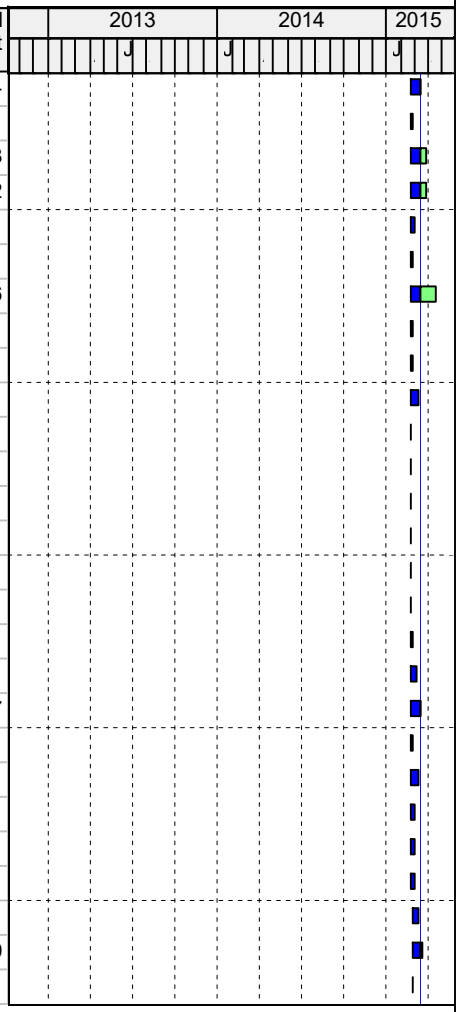



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6046 | Elev 6 - Fire alarm trim | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| EL-6048 | Elev 6 - Fire sprinkler trim | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| EL-6050 | Elev 6 - Install pit grates | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| L1L-8276 | Paint, prime & first coat finish | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| GB410-116 | Complete shower doors - Levels 4-10 | 2 | 0 | 25-Feb-15 A | 26-Feb-15 A | |
| L1BOH2-8114 | Ceiling grid & inspection | 4 | 1 | 26-Feb-15 A | 18-Mar-15 | 7 |
| SW-2066 | Porte Cochere - FRP planter curb | 2 | 0 | 26-Feb-15 A | 27-Feb-15 A | |
| L03-8684 | Pourback piping trench | 1 | 0 | 26-Feb-15 A | 26-Feb-15 A | |
| AS70 | ASI No. 70 - Site Illumination Plan | 0 | 0 | 26-Feb-15 A | | |
| I-5082 | ASI 70 - Site Illumination Plan | 0 | 0 | 26-Feb-15 A | | |
| L1BOH2-8200 | Paint, first coat finish | 1 | 1 | 26-Feb-15 A | 17-Mar-15 | 7 |
| CO-7220 | Cx - Start-Up - Common Space Heat Pump | 4 | 3 | 26-Feb-15 A | 18-Mar-15 | 20 |
| I-3102 | GWB, tape & finish ceiling at East Ballroom | 7 | 0 | 26-Feb-15 A | 06-Mar-15 A | |
| I-5124 | Dining feature wall - install plywood backing | 1 | 0 | 26-Feb-15 A | 26-Feb-15 A | |
| L03-8686 | Cure piping trench | 14 | 0 | 27-Feb-15 A | 12-Mar-15 A | |
| L1L-8114a | Install 9-wood celing supports - south of Grid K | 3 | 0 | 27-Feb-15 A | 04-Mar-15 A | |
| L1K-8124b | Flooring - epoxy - west end (including prep) | 7 | 0 | 27-Feb-15 A | 06-Mar-15 A | |
| CO-7104T | Fire Alarm & Smoke Control Pre-Testing (Tower) - Tow | 3 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7112T | City of Bellevue/3rd Party Fire Sprinkler Inspection / A | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7118T | City of Bellevue/3rd Party Fire Alarm Inspection / Appl | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7106T | City of Bellevue/3rd Party Smoke Control Testing (Tow | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7412 | Cx - Pressure Testing - GC Indicates Podium Complet | 0 | 0 | | 01-Mar-15 A | |
| CO-7416 | Cx - Pressure Testing - Pre-Walk with GC (Podium) [DI | 1 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7418 | Cx - Pressure Testing - GC Makes Corrections (Podiu | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7420 | Cx - Pressure Testing - Pressure Pre-Test (Podium) [D | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7422 | Cx - Pressure Testing -Corrections (Podium) [DELETE | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7424 | Cx - Pressure Testing - Pressure Final Test [DELETED | 1 | 0 | 01-Mar-15 A | 01-Mar-15 A | |

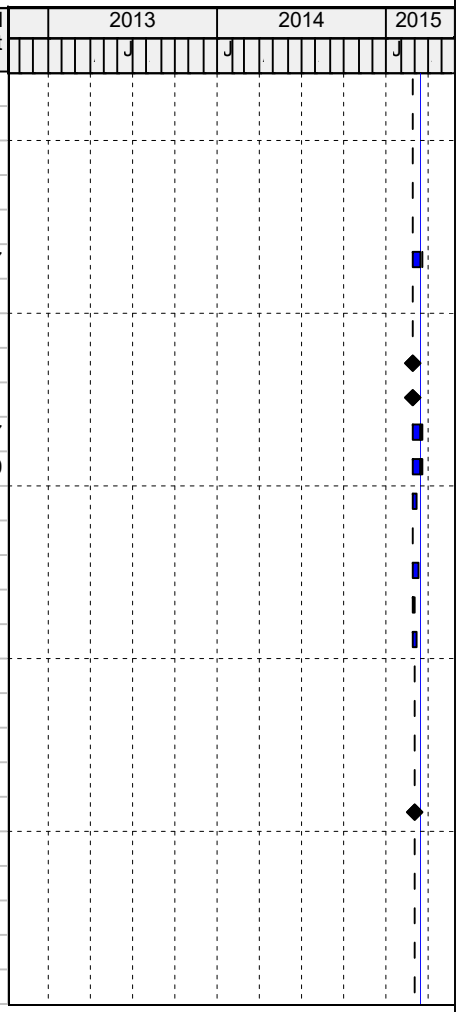



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7426 | Cx - Pressure Testing - Building Final Corrections [DEI | 1 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7142 | Fire Alarm System Device Testing - Podium [DELETEI | 7 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7428 | Cx - Pressure Testing - GC Indicates Tower Complete | 0 | 0 | | 01-Mar-15 A | |
| CO-7430 | Cx - Pressure Testing - Pre-Walk with GC (Tower) [DEI | 1 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7432 | Cx - Pressure Testing - GC Makes Corrections (Tower) | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7434 | Cx - Pressure Testing - Pressure Pre-Test (Tower) [DEI | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7436 | Cx - Pressure Testing -Corrections (Tower) [DELETED, | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| SW-2042 | Porte Cochere - Install trench drain | 3 | 0 | 02-Mar-15 A | 04-Mar-15 A | |
| SW-2128 | Zone 1 - FRP planter wall at NE corner | 8 | 0 | 02-Mar-15 A | 04-Mar-15 A | |
| SW-2130 | Zone 1 - Waterproof wall | 2 | 0 | 02-Mar-15 A | 02-Mar-15 A | |
| LL1-8136 | Ceramic tile in restrooms | 3 | 0 | 02-Mar-15 A | 04-Mar-15 A | |
| L1K-8218 | Floor prep | 2 | 0 | 02-Mar-15 A | 02-Mar-15 A | |
| L17-9012 | Complete Shower Surrounds | 2 | 1 | 02-Mar-15 A | 19-Mar-15 | 15 |
| LL2-2048 | Set Laundry Room equipment (BY OTHERS) | 1 | 0 | 03-Mar-15 A | 06-Mar-15 A | |
| L1K-8210 | Ceramic tile in restrooms | 7 | 2 | 03-Mar-15 A | 17-Mar-15 | 8 |
| MPT-1060 | Elevation 33/34 hat channel (east elevation, south er | 3 | 0 | 03-Mar-15 A | 10-Mar-15 A | |
| LL1-8142 | Plumbing fixtures & trim | 2 | 0 | 03-Mar-15 A | 04-Mar-15 A | |
| LL1-Z3-6038 | Paint ceiling at Food Prep (Dry Storage) | 2 | 0 | 03-Mar-15 A | 04-Mar-15 A | |
| L1B-6019 | Frame ceiling clouds | 7 | 0 | 03-Mar-15 A | 06-Mar-15 A | |
| LL1-Z3-8160 | Install doors & hardware at restrooms | 2 | 0 | 03-Mar-15 A | 04-Mar-15 A | |
| L17-9004 | Complete Flooring & Base | 3 | 2 | 03-Mar-15 A | 17-Mar-15 | 16 |
| CO-7116T | Fire Alarm Pre-Testing (Tower) - Tower Levels 4 thru 1( | 6 | 0 | 04-Mar-15 A | 05-Mar-15 A | |
| LL1-8150 | Install bathroom accessories | 2 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L1L-8142 | HVAC drops to 9-wood ceiling - north of Grid K | 2 | 0 | 04-Mar-15 A | 05-Mar-15 A | |
| L1L-8144 | Electrical drops to 9-wood ceiling - north of Grid K | 2 | 0 | 04-Mar-15 A | 05-Mar-15 A | |
| L1L-8146 | Fire sprinkler drops to 9-wood ceiling - north of Grid K | 2 | 0 | 04-Mar-15 A | 05-Mar-15 A | |
| CO-7110T | Fire Sprinkler Pre-Testing (Tower) - Tower Levels 4 thru | 6 | 0 | 05-Mar-15 A | 05-Mar-15 A | |

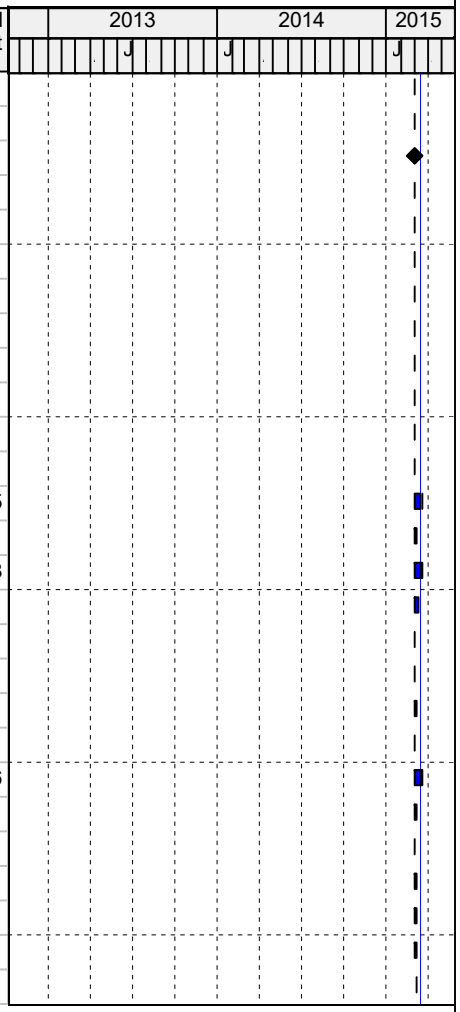



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7110T.1 | Fire Sprinkler Pre-Testing (Tower) - Tower Levels 3, 11 | 2 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| LL1-Z2-8150 | Install base at corridors | 3 | 0 | 05-Mar-15 A | 06-Mar-15 A | |
| L1L-8108 | GWB hang walls & ceilings (Bar) | 2 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L17-9000 | Complete GWB (1714 & 1718) | 5 | 0 | 06-Mar-15 A | 11-Mar-15 A | |
| LL1-Z2-8123 | Floor prep | 1 | 0 | 06-Mar-15 A | 06-Mar-15 A | |
| L1L-8110 | GWB tape & finish walls & ceilings (Bar) | 7 | 0 | 06-Mar-15 A | 12-Mar-15 A | |
| EL-1238 | Elev 1&2 - 30-day correction period | 30 | 21 | 07-Mar-15 A | 05-Apr-15 | 29 |
| L03-8624 | Fire sprinkler trim at Pool | 2 | 0 | 09-Mar-15 A | 09-Mar-15 A | |
| L11-7032 | Flooring - VCT (x42) | 1 | 0 | 09-Mar-15 A | 09-Mar-15 A | |
| SW-2212 | Zone 2 - FRP sidewalk panels | 3 | 0 | 09-Mar-15 A | 12-Mar-15 A | |
| SW-2048 | Porte Cochere - FRP Porte Cochere drive | 10 | 10 | 09-Mar-15 A | 27-Mar-15 | 18 |
| L03-8666 | Electrical trim & finish at ceiling at Pool | 2 | 0 | 09-Mar-15 A | 11-Mar-15 A | |
| CO-7139.1 | Install remaining devices & prep devices for testing - | 6 | 0 | 09-Mar-15 A | 12-Mar-15 A | |
| SW-2222 | Zone 2 - Install j-box at NE corner | 1 | 0 | 09-Mar-15 A | 09-Mar-15 A | |
| LL1-Z2-8146 | Floor prep at corridors | 2 | 0 | 09-Mar-15 A | 10-Mar-15 A | |
| L1L-8292 | GWB hang ceilings | 2 | 0 | 09-Mar-15 A | 10-Mar-15 A | |
| CO-7140.1 | Fire Alarm System Device Testing - Tower Levels 4 thr | 6 | 0 | 09-Mar-15 A | 12-Mar-15 A | |
| L1B-6025 | MEP drops at celing clouds (including inspection) | 7 | 3 | 09-Mar-15 A | 18-Mar-15 | 0 |
| L1L-8230 | Paint, prime & first coat finish | 3 | 0 | 10-Mar-15 A | 10-Mar-15 A | |
| LL2-2100 | Fire sprinkler drops to grid at Laundry | 1 | 0 | 10-Mar-15 A | 10-Mar-15 A | |
| LL1-Z2-8148 | Flooring - carpet at corridors | 3 | 0 | 10-Mar-15 A | 12-Mar-15 A | |
| L1B-8206 | Ceiling grid at West Ballrooms | 3 | 0 | 10-Mar-15 A | 11-Mar-15 A | |
| CM-1024 | Tower - "Clean/Punch" Complete - All Floors [DELETE | 0 | 0 | | 10-Mar-15 A | |
| MPT-1064 | Elevation 33/34 metal panels (east elevation, south e | 7 | 4 | 11-Mar-15 A | 19-Mar-15 | 8 |
| LL1-Z2-8160 | Flooring - carpet at Jr. Ballroom | 3 | 0 | 11-Mar-15 A | 13-Mar-15 A | |
| L1L-8258 | GWB tape & finish walls & ceilings | 7 | 1 | 11-Mar-15 A | 16-Mar-15 | 1 |
| L1BOH2-8120 | Wall coverings - vinyl | 3 | 1 | 12-Mar-15 A | 24-Mar-15 | 11 |

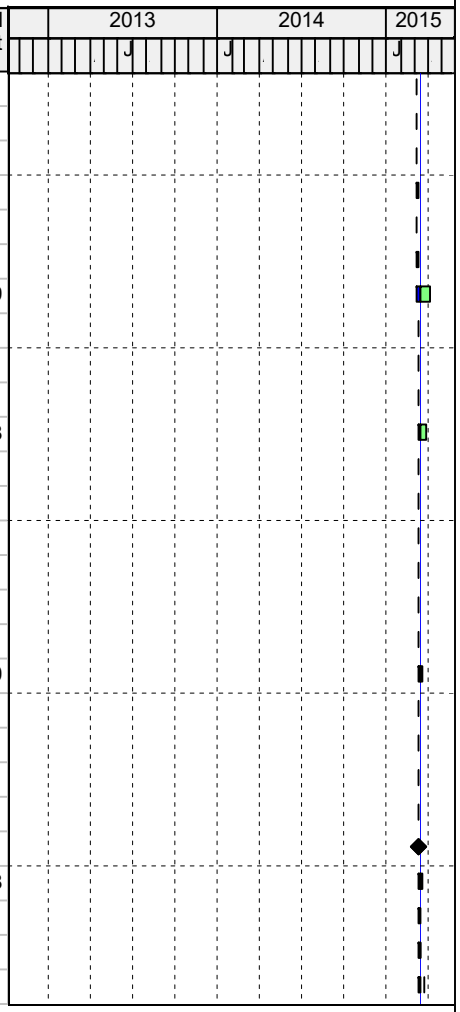


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-8208 | Ceiling grid at East Ballroom | 3 | 0 | 12-Mar-15 A | 13-Mar-15 A | |
| L17-9002 | Complete Painting | 2 | 0 | 12-Mar-15 A | 13-Mar-15 A | |
| L1L-8154 | Paint, prime & first finish coat (Bar) | 2 | 0 | 13-Mar-15 A | 13-Mar-15 A | |
| CO-7102T | Cx - DDC Point-To-Point - Central Plant | 5 | 5 | 16-Mar-15 | 20-Mar-15 | 34 |
| L17-7032 | Flooring - VCT (x42) | 1 | 1 | 16-Mar-15 | 16-Mar-15 | 17 |
| CO-7222 | Cx - Start-Up - Kitchen Exhaust Fans | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 21 |
| CO-7404 | Cx - FPT - Heat Pumps | 3 | 3 | 16-Mar-15 | 18-Mar-15 | 43 |
| LL1-Z3-FCC32 | Flooring - VCT at FCC | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 14 |
| MPT-1082 | Caulking - Elevation 48/49 (north elevation, east of 5 | 4 | 4 | 16-Mar-15 | 19-Mar-15 | 32 |
| CO-7116T.1 | Smoke Control Equipment Pre-Testing (Fans & Damp | 5 | 5 | 16-Mar-15 | 20-Mar-15 | 21 |
| LL1-8128 | Floor prep at Exercise Room | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 11 |
| L1K-8124a2 | Install doors & hardware | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 22 |
| L1L-8128 | Install die wall (Bar) | 3 | 3 | 16-Mar-15 | 18-Mar-15 | 8 |
| L1L-8232 | Wall coverings - vinyl | 5 | 5 | 16-Mar-15 | 20-Mar-15 | 14 |
| LL1-Z2-8144 | Install doors & hardware at corridors | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 22 |
| MPP-1060 | Install alcoves, south | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 41 |
| LL4-8136 | Clear out and clean parking area | 10 | 10 | 16-Mar-15 | 27-Mar-15 | 15 |
| LL3-8136 | Clear out and clean parking area | 10 | 10 | 16-Mar-15 | 27-Mar-15 | 15 |
| LL2-8152 | Clear out and clean parking area | 10 | 10 | 16-Mar-15* | 27-Mar-15 | 15 |
| L1L-8310 | Install 9-wood ceiling supports at Sitting Area | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 5 |
| L1L-8142a | HVAC drops to 9-wood ceiling - south of Grid K | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 0 |
| L1L-8144a | Electrical drops to 9-wood ceiling - south of Grid K | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 0 |
| L1L-8146a | Fire sprinkler drops to 9-wood ceiling - south of Grid K | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 0 |
| LL2-8156 | Remove job shacks | 1 | 1 | 16-Mar-15 | 16-Mar-15 | 37 |
| LL1-8186a | Wall coverings - complete vinyl at corridors | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 22 |
| L1K-8114a | Celing grid & inspection (west end) | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 17 |
| CM-1016c | CM - Owner FF+E "Build-Out" - Floors 6 & 7 | 7 | 7 | 16-Mar-15 | 22-Mar-15 | 17 |

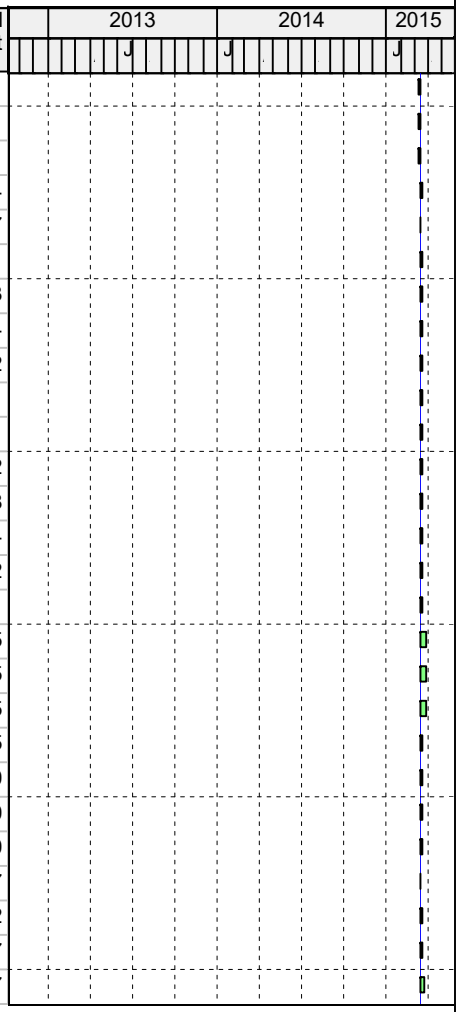



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8184 | Build Kitchen exhaust shaft | 5 | 5 | 16-Mar-15 | 20-Mar-15 | 5 |
| L1B-8174 | Complete grease duct insulation & inspect at Prefunc | 5 | 5 | 16-Mar-15 | 20-Mar-15 | 3 |
| L1B-8176 | Complete shaft wall at Prefunction 1 south end | 3 | 3 | 16-Mar-15 | 18-Mar-15 | 2 |
| LL2-2118 | Fabricate and deliver washing machine pedestal | 10 | 10 | 16-Mar-15 | 27-Mar-15 | 4 |
| L03-8622 | HVAC trim at Pool | 2 | 2 | 17-Mar-15 | 18-Mar-15 | 18 |
| L03-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 17-Mar-15* | 17-Mar-15 | 17 |
| L04-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 17-Mar-15 | 17-Mar-15 | 17 |
| L05-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 17-Mar-15 | 17-Mar-15 | 17 |
| CO-7226 | Cx - Start-Up - Misc. Equipment | 5 | 5 | 17-Mar-15 | 23-Mar-15 | 36 |
| MPT-1094 | Caulking - Elevation 32 (south elevation, east of man | 10 | 10 | 17-Mar-15 | 30-Mar-15 | 20 |
| I-1208 | Paint, prime & first coat finish | 2 | 2 | 17-Mar-15 | 18-Mar-15 | 1 |
| LL1-Z3-8206 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 17-Mar-15 | 19-Mar-15 | 11 |
| MPT-1120 | Cap metal at L12 Terrace | 2 | 2 | 17-Mar-15 | 18-Mar-15 | 30 |
| I-5084 | Zone 3 - FRP door apron at SE corner | 2 | 2 | 17-Mar-15 | 18-Mar-15 | 28 |
| L06-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 18-Mar-15 | 18-Mar-15 | 17 |
| L07-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 18-Mar-15 | 18-Mar-15 | 17 |
| L08-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 18-Mar-15 | 18-Mar-15 | 17 |
| LL1-Z3-FCC34 | Paint, final coat & touch-up up at FCC | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 15 |
| LL1-Z3-FCC36 | Install doors & hardware at FCC | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 15 |
| MPP-1020 | Elevation 18/19/21/22 & complete 45 (north elevatior | 12 | 12 | 18-Mar-15 | 31-Mar-15 | 8 |
| LL1-8138 | Flooring - install cork floor at Exercise Room | 3 | 3 | 18-Mar-15 | 20-Mar-15 | 11 |
| L1K-8130 | HVAC drops/trim at celing | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 17 |
| L1K-8202 | Ceiling grid at Janitorial | 1 | 1 | 18-Mar-15 | 18-Mar-15 | 8 |
| LL1-Z2-8136 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 18-Mar-15 | 20-Mar-15 | 17 |
| MPP-1064 | Install column at Pool | 1 | 1 | 18-Mar-15 | 18-Mar-15 | 18 |
| L1L-8312 | HVAC drops to 9-wood ceiling | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 5 |
| L1L-8314 | Electrical drops to 9-wood ceiling | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 5 |

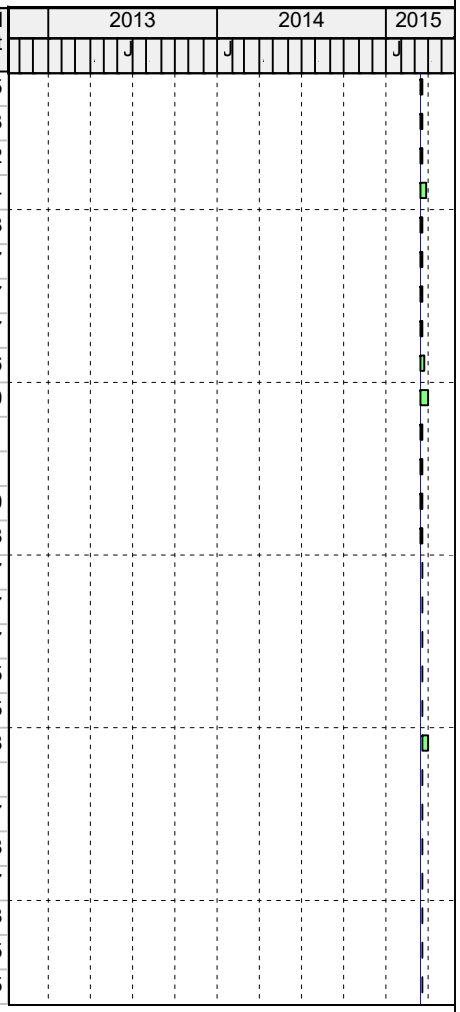



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8316 | Fire sprinkler drops to 9-wood ceiling | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 5 |
| L17-9006 | Complete Lighting & Electrical Trim | 2 | 2 | 18-Mar-15 | 19-Mar-15 | 16 |
| L17-9008 | Complete Fire Sprinkler Trim | 1 | 1 | 18-Mar-15 | 18-Mar-15 | 18 |
| L1BOH2-8126 | Install doors & hardware | 3 | 3 | 19-Mar-15 | 23-Mar-15 | 7 |
| L1BOH2-8204 | HVAC drops/trim at ceiling | 2 | 2 | 19-Mar-15 | 20-Mar-15 | 11 |
| MPP-1004 | Pool Area cornice metal | 11 | 11 | 19-Mar-15 | 31-Mar-15 | 18 |
| L09-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 19-Mar-15 | 19-Mar-15 | 17 |
| L10-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 19-Mar-15 | 19-Mar-15 | 17 |
| L11-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 19-Mar-15 | 19-Mar-15 | 17 |
| L02-8130 | Ceiling grid at south half | 3 | 3 | 19-Mar-15 | 23-Mar-15 | 6 |
| L17-8140 | Complete window sills | 1 | 1 | 19-Mar-15 | 19-Mar-15 | 17 |
| I-1206 | Install ceiling at Concierge Lounge (BOK) | 4 | 4 | 19-Mar-15 | 24-Mar-15 | 1 |
| MPT-1084 | Caulking - Hi-roof cornice metal | 6 | 6 | 19-Mar-15 | 26-Mar-15 | 27 |
| L1L-8136 | Install Peter Glassford art wall | 5 | 5 | 19-Mar-15 | 25-Mar-15 | 1 |
| L1L-8260 | Wall coverings - vinyl | 3 | 3 | 19-Mar-15 | 23-Mar-15 | 8 |
| LL2-2102 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 19-Mar-15 | 20-Mar-15 | 19 |
| L1K-8212 | Lighting & electrical trim at ceiling | 2 | 2 | 19-Mar-15 | 20-Mar-15 | 8 |
| L1B-6037 | GWB ceiling clouds | 5 | 5 | 19-Mar-15 | 25-Mar-15 | 0 |
| L02-8154 | Wall coverings - vinyl at north half | 3 | 3 | 19-Mar-15 | 23-Mar-15 | 6 |
| MPT-1110 | Cap metal at hi-roof | 3 | 3 | 19-Mar-15 | 23-Mar-15 | 30 |
| L1L-8148 | Electrical rough-in at die wall (Bar) | 4 | 4 | 19-Mar-15 | 24-Mar-15 | 10 |
| L1L-8150 | Plumbing rough-in at die wall (Bar) | 4 | 4 | 19-Mar-15 | 24-Mar-15 | 8 |
| L1B-8178 | Complete framing & MEP at Prefunction 1 south end | 3 | 3 | 19-Mar-15 | 23-Mar-15 | 2 |
| L12-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 20-Mar-15 | 20-Mar-15 | 17 |
| L14-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 20-Mar-15 | 20-Mar-15 | 17 |
| L15-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 20-Mar-15 | 20-Mar-15 | 17 |
| RF-4070 | TR - Terrace Roof - Install American Hydrotech assem | 3 | 3 | 20-Mar-15 | 24-Mar-15 | 29 |

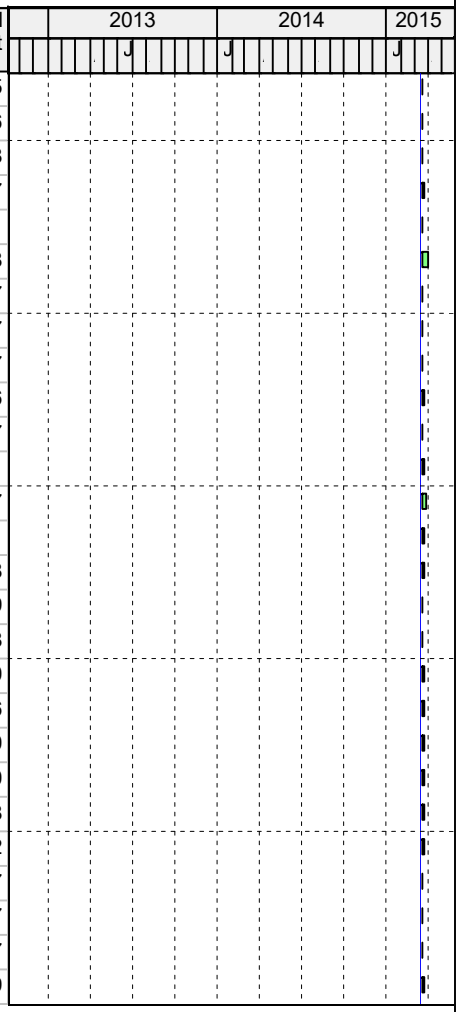


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7230 | Cx - TAB - Air Balancing | 15 | 15 | 20-Mar-15 | 09-Apr-15 | 19 |
| LL1-Z3-FCC38 | Final clean and punch list at FCC | 3 | 3 | 20-Mar-15 | 24-Mar-15 | 15 |
| L1K-8120 | Lighting & electrical trim at ceiling | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 17 |
| MPT-1096 | Caulking - Elevation 33/34 (east elevation, south end | 10 | 10 | 20-Mar-15 | 02-Apr-15 | 17 |
| L1K-8160 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 17 |
| L1L-8308 | Floor (stair) prep | 1 | 1 | 20-Mar-15 | 20-Mar-15 | 4 |
| L1L-8318 | Install 9-wood ceiling at Sitting Area | 3 | 3 | 20-Mar-15 | 24-Mar-15 | 5 |
| L1K-8128 | Install Kitchen equipment (BY OTHERS) | 5 | 5 | 23-Mar-15* | 27-Mar-15 | 9 |
| L16-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 23-Mar-15 | 23-Mar-15 | 17 |
| L17-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 23-Mar-15 | 23-Mar-15 | 17 |
| L1K-8206 | Install toilets at restrooms | 2 | 2 | 23-Mar-15 | 24-Mar-15 | 8 |
| L1BOH2C-6024 | Lighting & electrical trim at ceiling | 2 | 2 | 23-Mar-15 | 24-Mar-15 | 11 |
| L02-8148 | Paint at Locker Rooms | 2 | 2 | 23-Mar-15 | 24-Mar-15 | 5 |
| LL1-8130 | Install base | 3 | 3 | 23-Mar-15 | 25-Mar-15 | 11 |
| L1BOH2C-6026 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 23-Mar-15 | 24-Mar-15 | 11 |
| CN-1000 | Install exterior canopies - steel | 5 | 5 | 23-Mar-15* | 27-Mar-15 | 6 |
| LL1-Z2-8142a | Wall coverings - complete vinyl at corridors | 2 | 2 | 23-Mar-15 | 24-Mar-15 | 19 |
| CM-1016d | CM - Owner FF+E "Build-Out" - Floors 8 & 9 | 7 | 7 | 23-Mar-15 | 29-Mar-15 | 17 |
| CO-7116.1 | Smoke Control Equipment Pre-Testing (Fans & Damp | 5 | 5 | 23-Mar-15 | 27-Mar-15 | 21 |
| I-6014 | Install temporary partition at corridor | 1 | 1 | 23-Mar-15* | 23-Mar-15 | 16 |
| L1BOH2-8116 | Finish carpentry/millwork | 5 | 5 | 24-Mar-15 | 30-Mar-15 | 7 |
| L1K-8122 | Fire sprinkler drops/trim at ceiling | 1 | 1 | 24-Mar-15 | 24-Mar-15 | 17 |
| L1L-8138 | Flooring - epoxy floor (Bar) | 5 | 5 | 24-Mar-15 | 30-Mar-15 | 4 |
| LL1-Z3-8128 | Flooring - VCT | 3 | 3 | 24-Mar-15 | 26-Mar-15 | 11 |
| L02-8156 | Install doors & hardware at north half | 3 | 3 | 24-Mar-15 | 26-Mar-15 | 11 |
| L02-8158 | Ceiling grid at north half | 3 | 3 | 24-Mar-15 | 26-Mar-15 | 6 |
| L1L-8140a | Install 9-wood ceiling - south of Grid K | 4 | 4 | 24-Mar-15 | 27-Mar-15 | 0 |

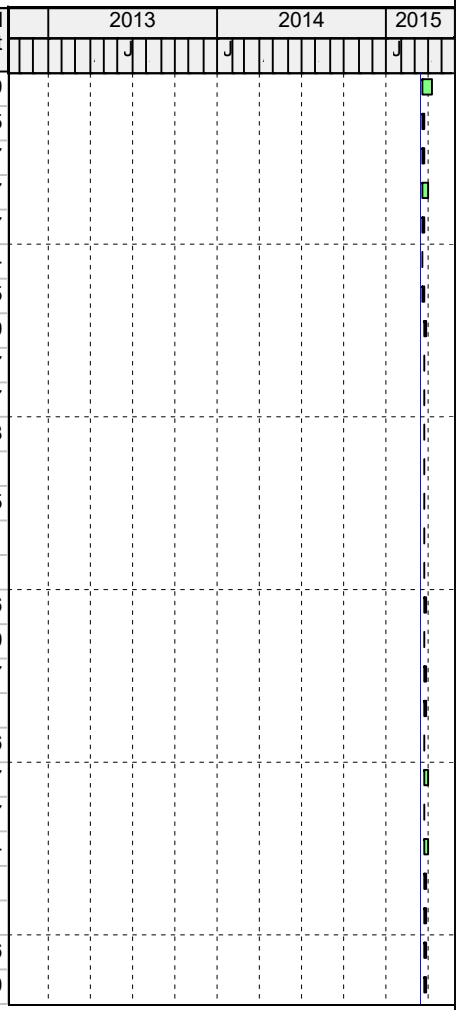


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8206a | Flooring - carpet at corridors (E-W leg) | 2 | 2 | 24-Mar-15 | 25-Mar-15 | 16 |
| L17-9016 | Complete Shower Doors | 2 | 2 | 24-Mar-15 | 25-Mar-15 | 15 |
| L1BOH2-8112 | Fire sprinkler drops/trim at ceiling | 1 | 1 | 25-Mar-15 | 25-Mar-15 | 12 |
| LL1-Z3-FCC40 | Install Knox Box at FCC | 2 | 2 | 25-Mar-15 | 26-Mar-15 | 15 |
| L02-8142 | Ceiling grid at Locker Rooms | 3 | 3 | 25-Mar-15 | 27-Mar-15 | 5 |
| L1L-8238 | HVAC drops/trim at celing | 2 | 2 | 25-Mar-15 | 26-Mar-15 | 6 |
| L1L-8242 | Finish carpentry/millwork (including front desk) | 12 | 12 | 25-Mar-15 | 09-Apr-15 | 5 |
| L1L-8266 | HVAC drops/trim at celing | 2 | 2 | 25-Mar-15 | 26-Mar-15 | 1 |
| L1K-8125 | Floor prep | 2 | 2 | 25-Mar-15 | 26-Mar-15 | 11 |
| L1BOH2-8123 | Floor prep | 2 | 2 | 25-Mar-15 | 26-Mar-15 | 11 |
| L1L-8239 | Floor prep | 2 | 2 | 25-Mar-15 | 26-Mar-15 | 5 |
| L1L-8206 | Lighting & electrical trim at ceilings - north of Grid K | 2 | 2 | 25-Mar-15 | 26-Mar-15 | 1 |
| L1K-8220 | Install countertops in restrooms | 2 | 2 | 25-Mar-15 | 26-Mar-15 | 11 |
| L1K-8222 | Install toilet partitions | 4 | 4 | 25-Mar-15 | 30-Mar-15 | 8 |
| LL1-Z3-8158 | Install toilet partitions | 4 | 4 | 25-Mar-15 | 30-Mar-15 | 11 |
| MPT-1038 | Install louvers, north | 3 | 3 | 26-Mar-15 | 28-Mar-15 | 27 |
| L02-8140 | Lighting & electrical trim at south half | 2 | 2 | 26-Mar-15 | 27-Mar-15 | 6 |
| LL1-8144 | Finish carpentry/millwork | 5 | 5 | 26-Mar-15 | 01-Apr-15 | 11 |
| L1B-8202 | Wall coverings - vinyl at Ballrooms | 5 | 5 | 26-Mar-15 | 01-Apr-15 | 5 |
| L1L-8264 | Lighting & electrical trim at ceilings | 3 | 3 | 26-Mar-15 | 30-Mar-15 | 1 |
| L1L-8280 | Install Peter Glassford art wall | 5 | 5 | 26-Mar-15 | 01-Apr-15 | 1 |
| L1L-8123 | Floor prep - north of Grid K | 2 | 2 | 26-Mar-15 | 27-Mar-15 | 1 |
| MPT-1106 | Install alcoves, north | 3 | 3 | 26-Mar-15 | 28-Mar-15 | 20 |
| L1L-8116a | Finish carpentry/millwork - south of Grid K | 5 | 5 | 26-Mar-15 | 01-Apr-15 | 1 |
| CO-7139.2 | Install Fire Alarm Devices & Map to Panel - Tower Lev | 2 | 2 | 26-Mar-15 | 27-Mar-15 | 16 |
| L1BOH2-8124 | Flooring - VCT | 3 | 3 | 27-Mar-15 | 31-Mar-15 | 11 |
| LL1-Z3-FCC22 | Final inspections by CoB and Fire Marshall | 2 | 2 | 27-Mar-15 | 30-Mar-15 | 15 |

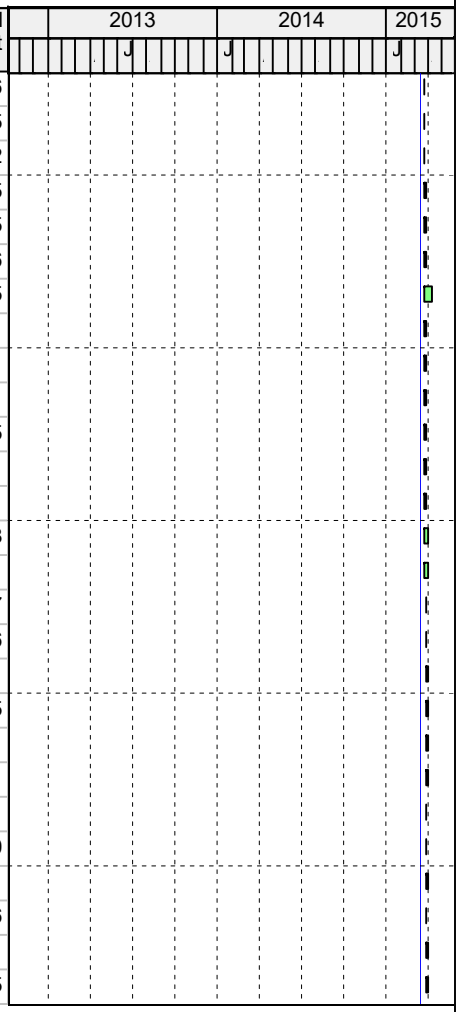



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8236 | Lighting & electrical trim at ceilings | 3 | 3 | 27-Mar-15 | 31-Mar-15 | 6 |
| L1L-8286 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 27-Mar-15 | 31-Mar-15 | 6 |
| L1L-8298 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 27-Mar-15 | 30-Mar-15 | 2 |
| L1L-8302 | Lighting & electrical trim at ceilings | 3 | 3 | 27-Mar-15 | 31-Mar-15 | 11 |
| L1L-8304 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 3 | 27-Mar-15 | 31-Mar-15 | 11 |
| L02-8160 | HVAC drops/trim at north half | 2 | 2 | 27-Mar-15 | 30-Mar-15 | 6 |
| L1K-8224 | Install sinks at restrooms | 2 | 2 | 27-Mar-15 | 30-Mar-15 | 11 |
| MPP-1050 | Columns at Porte Cochere | 4 | 4 | 28-Mar-15 | 01-Apr-15 | 22 |
| SW-2122 | Zone 1 - Install landscaping & irrigation | 10 | 10 | 30-Mar-15 | 10-Apr-15 | 21 |
| SW-2218 | Zone 2 - Install landscaping & irrigation | 10 | 10 | 30-Mar-15 | 10-Apr-15 | 21 |
| L1K-8128a | Kitchen Equipment Final Connections | 5 | 5 | 30-Mar-15 | 03-Apr-15 | 9 |
| MPP-1048 | Caulking - Porte Cochere cornice metal | 3 | 3 | 30-Mar-15 | 01-Apr-15 | 23 |
| CO-7104T.1 | Fire Alarm/Smoke Control Pre-Functional Testing - To | 10 | 10 | 30-Mar-15 | 10-Apr-15 | 16 |
| L02-8145 | MEP drops to framed ceiling (including inspections) | 2 | 2 | 30-Mar-15 | 31-Mar-15 | 5 |
| SW-2330 | Zone 3 - Landscaping & irrigation | 10 | 10 | 30-Mar-15 | 10-Apr-15 | 21 |
| LL2-8106b | Pinned insulation at ramp at Garage & dry shack area | 3 | 3 | 30-Mar-15 | 01-Apr-15 | 28 |
| L02-8114 | Floor prep at south half | 2 | 2 | 30-Mar-15 | 31-Mar-15 | 6 |
| LL1-Z3-8156 | Install countertops at restrooms | 2 | 2 | 30-Mar-15 | 31-Mar-15 | 8 |
| MPT-1118 | Cap metal - Pool terrace | 3 | 3 | 30-Mar-15 | 01-Apr-15 | 23 |
| L1L-8204a | HVAC trim at ceiling - south of Grid K | 1 | 1 | 30-Mar-15 | 30-Mar-15 | 0 |
| L1K-8128b | Ansul system final connections | 5 | 5 | 30-Mar-15 | 03-Apr-15 | 9 |
| LL4-8138 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 30-Mar-15 | 03-Apr-15 | 15 |
| LL3-8138 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 30-Mar-15 | 03-Apr-15 | 15 |
| I-6012 | Core drill & install new floor drain and piping | 2 | 2 | 30-Mar-15 | 31-Mar-15 | 0 |
| CM-1016b | CM - Owner FF&E "Build-Out" - Floors 10 & 11 | 7 | 7 | 30-Mar-15 | 05-Apr-15 | 17 |
| LL1-8116a | Install countertops (owner-furnished) | 2 | 2 | 30-Mar-15 | 31-Mar-15 | 12 |
| LL1-Z2-8116a | Install countertops (owner-furnished) | 1 | 1 | 30-Mar-15 | 30-Mar-15 | 13 |

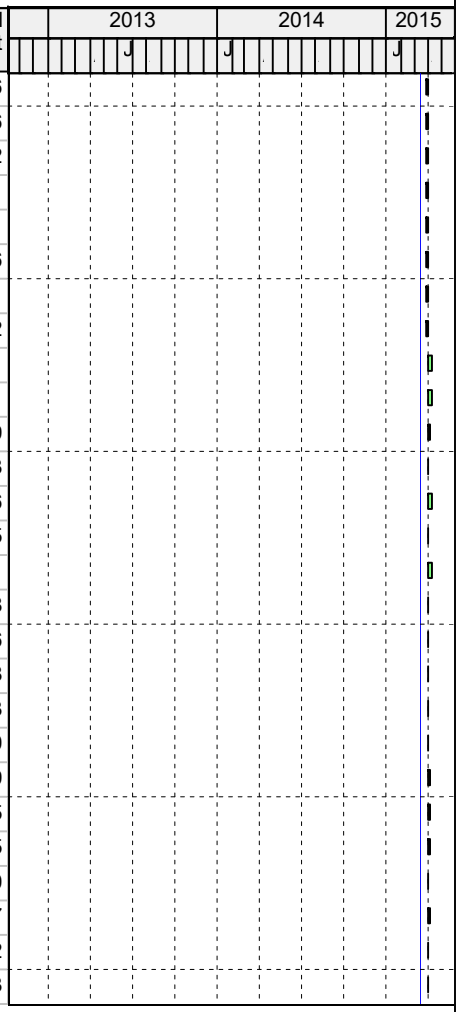



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CN-1004 | Field measure & fabricate canopy glass | 15 | 15 | 30-Mar-15 | 17-Apr-15 | 6 |
| LL2-2114 | Install washing machine pedestal | 2 | 2 | 30-Mar-15 | 31-Mar-15 | 4 |
| L1BOH2-8124a | Install base | 5 | 5 | 31-Mar-15 | 06-Apr-15 | 7 |
| CO-7260 | Cx - Start-Up - Ballroom AAON RTU | 1 | 1 | 31-Mar-15 | 31-Mar-15 | 16 |
| L1L-8262 | Fire sprinkler trim at ceilings | 1 | 1 | 31-Mar-15 | 31-Mar-15 | 2 |
| I-1210 | Floor prep | 2 | 2 | 31-Mar-15 | 01-Apr-15 | 1 |
| L02-8162 | Lighting & electrical trim at north half | 2 | 2 | 31-Mar-15 | 01-Apr-15 | 6 |
| L02-8164 | Fire alarm trim (speaker/strobe & smoke detector bas | 2 | 2 | 31-Mar-15 | 01-Apr-15 | 6 |
| L1L-8152 | Install ceiling (Bar) | 4 | 4 | 31-Mar-15 | 03-Apr-15 | 4 |
| L1L-8206a | Lighting & elecrical trim at ceilings - south of Grid K | 2 | 2 | 31-Mar-15 | 01-Apr-15 | 0 |
| CO-7264 | Cx - Start-Up - Lobby Trane TRU (2) | 2 | 2 | 01-Apr-15 | 02-Apr-15 | 20 |
| CO-7132 | Cx - DDC Point-To-Point - Ballroom VAV | 4 | 4 | 01-Apr-15 | 06-Apr-15 | 16 |
| MPP-1040 | Caulking - Pool Area & Ballroom cornice metal | 8 | 8 | 01-Apr-15 | 10-Apr-15 | 15 |
| L02-8150 | Install doors & hardware at Locker Rooms | 1 | 1 | 01-Apr-15 | 01-Apr-15 | 8 |
| LL1-Z3-8152 | Complete MEP trim | 2 | 2 | 01-Apr-15 | 02-Apr-15 | 12 |
| L1L-8234 | Fire sprinkler trim at ceilings | 1 | 1 | 01-Apr-15 | 01-Apr-15 | 6 |
| L1B-8142 | Paint, prime & first coat finish walls & ceilings at corrid | 2 | 2 | 01-Apr-15 | 02-Apr-15 | 2 |
| L1L-8306 | Fire sprinkler trim | 1 | 1 | 01-Apr-15 | 01-Apr-15 | 11 |
| L02-8152 | Flooring - VCT at south half | 2 | 2 | 01-Apr-15 | 02-Apr-15 | 8 |
| L02-8166 | Fire sprinkler trim at north half | 2 | 2 | 01-Apr-15 | 02-Apr-15 | 6 |
| L02-8168 | Floor prep at north half | 2 | 2 | 01-Apr-15 | 02-Apr-15 | 6 |
| L1L-8123a | Floor prep - south of Grid K | 2 | 2 | 01-Apr-15 | 02-Apr-15 | 0 |
| L03-8669 | Install anchor bolts for trench drain | 1 | 1 | 01-Apr-15 | 01-Apr-15 | 0 |
| LL1-Z3-8162 | Install sinks at Restrooms | 2 | 2 | 01-Apr-15 | 02-Apr-15 | 8 |
| LL2-2112 | Set washing machines | 1 | 1 | 01-Apr-15 | 01-Apr-15 | 4 |
| LL2-2116 | Relocate dryers and remove floor coping at dryer area | 3 | 3 | 01-Apr-15 | 03-Apr-15 | 4 |
| I-1202 | Flooring - tile & carpet at Concierge Lounge | 7 | 7 | 02-Apr-15 | 10-Apr-15 | 1 |

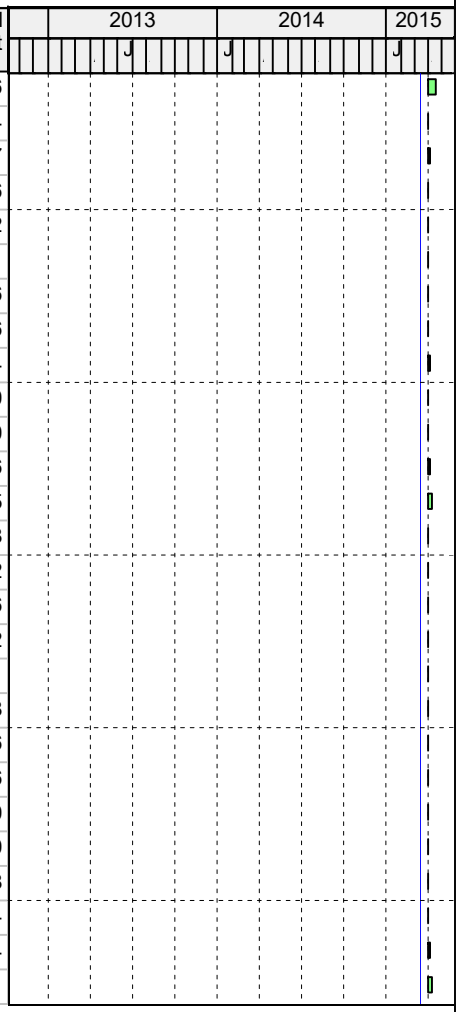



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-8146 | Complete MEP trim | 2 | 2 | 02-Apr-15 | 03-Apr-15 | 11 |
| LL1-8148 | Complete acoustical ceiling tile | 2 | 2 | 02-Apr-15 | 03-Apr-15 | 11 |
| L1L-8278 | Flooring - tile at stair treads | 10 | 10 | 02-Apr-15 | 15-Apr-15 | 1 |
| LL1-8188 | Complete paint final coat & touch-up | 2 | 2 | 02-Apr-15 | 03-Apr-15 | 11 |
| L1L-8203 | Complete MEP trim | 2 | 2 | 02-Apr-15 | 03-Apr-15 | 14 |
| MPP-1018 | Elevation A/B/C (Porte Cochere wall panels) | 2 | 2 | 02-Apr-15 | 03-Apr-15 | 22 |
| L1L-8112a | Fire sprinkler trim - south of Grid K | 1 | 1 | 02-Apr-15 | 02-Apr-15 | 0 |
| L1L-8118a | Fire alarm trim (spreaker strobe & smoke detector bas | 1 | 1 | 02-Apr-15 | 02-Apr-15 | 0 |
| L03-8682 | Install waterproofing and protection layer | 3 | 3 | 02-Apr-15 | 06-Apr-15 | 0 |
| SW-2050 | Street - Grind and overlay | 3 | 3 | 02-Apr-15 | 06-Apr-15 | 21 |
| L1K-8208 | Install restroom accessories | 2 | 2 | 03-Apr-15 | 06-Apr-15 | 8 |
| LL1-Z3-8146 | Install restroom accessories | 2 | 2 | 03-Apr-15 | 06-Apr-15 | 8 |
| MPP-1038 | Podium Signs, West | 5 | 5 | 03-Apr-15 | 09-Apr-15 | 17 |
| MPT-1074 | Tower Sign, South (El 32) | 5 | 5 | 03-Apr-15 | 09-Apr-15 | 17 |
| L1BOH2-8128 | Flooring - carpet | 3 | 3 | 03-Apr-15 | 07-Apr-15 | 7 |
| L1B-8162 | Install doors & hardware at corridors | 2 | 2 | 03-Apr-15 | 06-Apr-15 | 8 |
| L02-8170 | Flooring - VCT at north half | 3 | 3 | 03-Apr-15 | 07-Apr-15 | 6 |
| L1L-8124b | Flooring - wood - south of Grid K | 5 | 5 | 03-Apr-15 | 09-Apr-15 | 0 |
| LL1-Z3-8136 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 03-Apr-15 | 09-Apr-15 | 12 |
| L1K-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 06-Apr-15 | 07-Apr-15 | 9 |
| L1L-8124a | Install base | 3 | 3 | 06-Apr-15 | 08-Apr-15 | 11 |
| CO-7138 | Elevator Finals with AHJ | 5 | 5 | 06-Apr-15 | 10-Apr-15 | 26 |
| L1L-8130 | Install bar and back bar | 10 | 10 | 06-Apr-15 | 17-Apr-15 | 4 |
| MPP-1056 | Caulking - Porte Cochere walls & columns | 3 | 3 | 06-Apr-15 | 08-Apr-15 | 18 |
| LL1-8190 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 06-Apr-15 | 10-Apr-15 | 11 |
| EL-1240 | Elev 1&2 - Final elevator inspection | 2 | 2 | 06-Apr-15 | 07-Apr-15 | 21 |
| CM-1016e | CM - Owner FF+E "Build-Out" - Floors 12 & 14 | 7 | 7 | 06-Apr-15 | 12-Apr-15 | 17 |

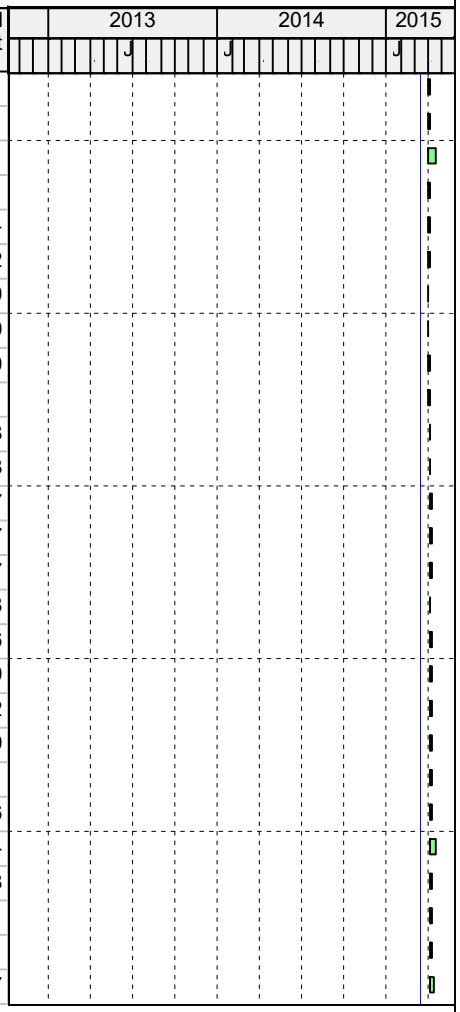



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2110 | Restore epoxy flooring at dryer location | 5 | 5 | 06-Apr-15 | 10-Apr-15 | 4 |
| CO-7134 | Cx - DDC Point-To-Point - Ballroom RTU (2) | 2 | 2 | 07-Apr-15 | 08-Apr-15 | 16 |
| L03-8670 | Installl trench drains at Pool | 2 | 2 | 07-Apr-15 | 08-Apr-15 | 0 |
| L1K-8154 | Complete acoustical ceiling tile | 2 | 2 | 07-Apr-15 | 08-Apr-15 | 8 |
| L1K-8156 | Complete MEP trim | 2 | 2 | 07-Apr-15 | 08-Apr-15 | 8 |
| L1K-8158 | Complete paint final coat & touch-up | 2 | 2 | 07-Apr-15 | 08-Apr-15 | 8 |
| L1B-8129 | Floor prep | 2 | 2 | 07-Apr-15 | 08-Apr-15 | 0 |
| LL1-Z3-8150 | Complete paint final coat & touch-up | 2 | 2 | 07-Apr-15 | 08-Apr-15 | 8 |
| LL1-Z3-8154 | Complete MEP trim | 2 | 2 | 07-Apr-15 | 08-Apr-15 | 8 |
| L1B-8146 | HVAC drops/trim at corridors | 2 | 2 | 07-Apr-15 | 08-Apr-15 | 3 |
| SW-2068 | Street - Striping | 2 | 2 | 07-Apr-15 | 08-Apr-15 | 21 |
| L1BOH2-8140 | Acoustical ceiling tile | 2 | 2 | 08-Apr-15 | 09-Apr-15 | 7 |
| L1BOH2-8201 | Paint, final coat & touch-up | 2 | 2 | 08-Apr-15 | 09-Apr-15 | 7 |
| L1BOH2-8118 | Complete MEP trim | 2 | 2 | 08-Apr-15 | 09-Apr-15 | 7 |
| CO-7406 | Cx - FPT - MUA, RTU, VAV and Exhaust Fans | 5 | 5 | 08-Apr-15 | 14-Apr-15 | 19 |
| L1B-8144 | Wall coverings - vinyl at corridors | 3 | 3 | 08-Apr-15 | 10-Apr-15 | 2 |
| L1B-8148 | Lighting & electrical trim at corridors | 2 | 2 | 08-Apr-15 | 09-Apr-15 | 3 |
| L1B-8150 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 08-Apr-15 | 09-Apr-15 | 4 |
| L1B-8156 | Install base at corridors | 5 | 5 | 08-Apr-15 | 14-Apr-15 | 2 |
| L02-8172 | Finish carpentry/millwork at north half | 1 | 1 | 08-Apr-15 | 08-Apr-15 | 6 |
| L1B-8128 | Install base at Ballrooms | 5 | 5 | 09-Apr-15 | 15-Apr-15 | 0 |
| CO-7136 | Cx - DDC Point-To-Point - MUA AAON Start-Up (8) | 5 | 5 | 09-Apr-15 | 15-Apr-15 | 16 |
| L03-8672 | Prep & pour pool topping slab | 2 | 2 | 09-Apr-15 | 10-Apr-15 | 3 |
| LL1-Z2-8162 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 09-Apr-15 | 15-Apr-15 | 8 |
| L1K-8166 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 09-Apr-15 | 15-Apr-15 | 8 |
| SW-2070 | Street - Signage | 2 | 2 | 09-Apr-15 | 10-Apr-15 | 21 |
| L02-8138 | Complete acoustical ceiling tile | 2 | 2 | 10-Apr-15 | 13-Apr-15 | 5 |

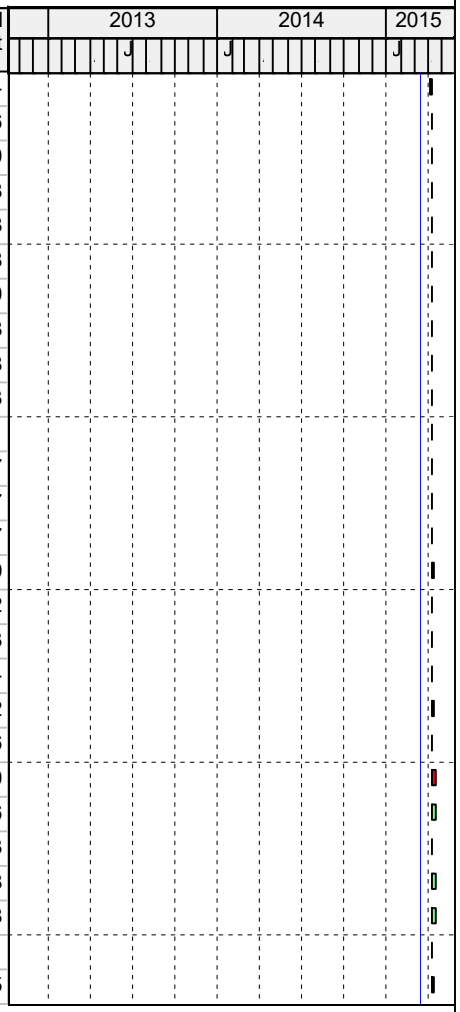


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8240 | Flooring - tile & base | 10 | 10 | 10-Apr-15 | 23-Apr-15 | 0 |
| L1L-8244 | Complete MEP trim | 2 | 2 | 10-Apr-15 | 13-Apr-15 | 8 |
| L1B-8152 | Fire sprinkler drops/trim at corridors | 1 | 1 | 10-Apr-15 | 10-Apr-15 | 4 |
| L1B-8160 | Floor prep | 2 | 2 | 10-Apr-15 | 13-Apr-15 | 3 |
| L1L-8288 | Paint, final coat & touch-up | 2 | 2 | 10-Apr-15 | 13-Apr-15 | 8 |
| CO-7154 | Final Inspection - Mechanical | 5 | 5 | 10-Apr-15 | 16-Apr-15 | 22 |
| L1BOH2-8136 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 10-Apr-15 | 16-Apr-15 | 7 |
| I-1204 | Finish carpentry/millwork at Concierge Lounge | 6 | 6 | 13-Apr-15 | 20-Apr-15 | 1 |
| LL2-2050 | Laundry Room equipment final connections (MEP) | 3 | 3 | 13-Apr-15 | 15-Apr-15 | 4 |
| L03-8630 | Install doors & hardware at Pool | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 11 |
| RF-4066 | Pool Green Roof - Install decorative metal railing | 3 | 3 | 13-Apr-15 | 15-Apr-15 | 15 |
| CO-7160 | Generator - Cx generator/owner training | 3 | 3 | 13-Apr-15 | 15-Apr-15 | 25 |
| LL2-8144 | Complete acoustical ceiling tile | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 4 |
| L1B-8154 | Finish carpentry/millwork at corridors | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 2 |
| L03-8674 | Install storefront at Pool entry | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 13 |
| CO-7146 | Final Inspection - Clear & Grade | 5 | 5 | 13-Apr-15 | 17-Apr-15 | 21 |
| CM-1016f | CM - Owner FF+E "Build-Out" - Floors 15 & 16 | 7 | 7 | 13-Apr-15 | 19-Apr-15 | 17 |
| L1B-8130 | Flooring - VCT at service corridor and A/V room | 3 | 3 | 14-Apr-15 | 16-Apr-15 | 3 |
| L02-8182 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 14-Apr-15 | 20-Apr-15 | 5 |
| LL2-8154 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 15-Apr-15 | 21-Apr-15 | 4 |
| L1L-8120 | Plumbing fixtures & trim (Bar) | 2 | 2 | 16-Apr-15 | 17-Apr-15 | 4 |
| L1L-8122 | Electrical trim & finish at bar (bar area final connectior | 2 | 2 | 16-Apr-15 | 17-Apr-15 | 4 |
| L03-8618 | Ceramic tile at pool area | 8 | 8 | 16-Apr-15 | 27-Apr-15 | 0 |
| L03-8640 | Prep and install pool plaster | 3 | 3 | 16-Apr-15 | 20-Apr-15 | 9 |
| RF-4068 | Pool Green Roof - Install American Hydrotech assemI | 3 | 3 | 16-Apr-15 | 20-Apr-15 | 15 |
| CO-7402 | Cx - FPT - Central Plant | 2 | 2 | 16-Apr-15 | 17-Apr-15 | 16 |
| L1L-8282 | Finish carpentry/millwork | 5 | 5 | 16-Apr-15 | 22-Apr-15 | 1 |

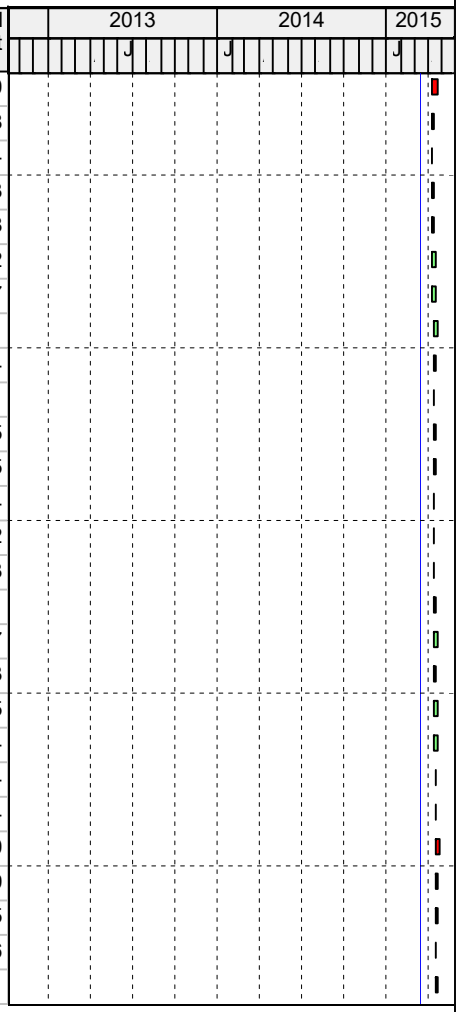



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7156 | Final Inspection - Health Department (Kitchens) | 5 | 5 | 16-Apr-15 | 22-Apr-15 | 18 |
| L1BOH2-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 4 | 4 | 17-Apr-15 | 22-Apr-15 | 12 |
| L1B-8158 | Flooring - carpet at corridors | 3 | 3 | 17-Apr-15 | 21-Apr-15 | 0 |
| CM-1016a | CM - Owner FF+E "Build-Out" - Floors 3 & 17 | 7 | 7 | 20-Apr-15 | 26-Apr-15 | 24 |
| CO-7408 | Cx - FPT - Garage Exhaust Fans | 1 | 1 | 20-Apr-15 | 20-Apr-15 | 16 |
| SW-2228 | Zone 2 - Pull wire and install light poles | 5 | 5 | 20-Apr-15 | 24-Apr-15 | 11 |
| SW-2232 | Zone 2 - Replace luminaire north of 3rd | 1 | 1 | 20-Apr-15 | 20-Apr-15 | 15 |
| SW-2328 | Zone 3 - Pull wire and install light poles | 5 | 5 | 20-Apr-15 | 24-Apr-15 | 11 |
| SW-2056 | Zone 4 - Pull wire and replace luminaires on 110th | 5 | 5 | 20-Apr-15 | 24-Apr-15 | 11 |
| CO-7152 | Final Inspection - Plumbing | 5 | 5 | 20-Apr-15 | 24-Apr-15 | 16 |
| CN-1002 | Install exterior canopies - glass | 5 | 5 | 20-Apr-15 | 24-Apr-15 | 6 |
| L03-8642 | Fill pool | 1 | 1 | 21-Apr-15 | 21-Apr-15 | 9 |
| L03-8644 | Connect, startup & adjust pool equipment | 10 | 10 | 21-Apr-15 | 04-May-15 | 9 |
| CO-7410 | Cx - FPT - Misc Equipment | 4 | 4 | 21-Apr-15 | 24-Apr-15 | 16 |
| CO-7141 | Install Fire Alarm Devices & Map to Panel - Podium | 5 | 5 | 21-Apr-15 | 27-Apr-15 | 0 |
| L1L-8268 | Complete MEP trim | 2 | 2 | 21-Apr-15 | 22-Apr-15 | 1 |
| L1L-8284 | Install handrails | 2 | 2 | 21-Apr-15 | 22-Apr-15 | 1 |
| L1L-8300 | Paint, final coat & touch-up | 2 | 2 | 21-Apr-15 | 22-Apr-15 | 1 |
| L1BOH2-8134 | Final Cleaning | 2 | 2 | 22-Apr-15 | 23-Apr-15 | 12 |
| L1B-8136 | Complete MEP trim | 2 | 2 | 22-Apr-15 | 23-Apr-15 | 0 |
| L03-8638 | Install pool deck and ADA lift | 3 | 3 | 23-Apr-15 | 27-Apr-15 | 14 |
| L1BOH2-81214 | L1, Zone 3 Complete | 0 | 0 | | 23-Apr-15 | 12 |
| CO-7150 | Final Inspection - Electrical | 5 | 5 | 24-Apr-15 | 30-Apr-15 | 12 |
| L1B-8172 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 24-Apr-15 | 30-Apr-15 | 0 |
| L1L-8156 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 24-Apr-15 | 30-Apr-15 | 0 |
| CO-7144 | Final Inspection - Transportation (Right-Of-Way) | 5 | 5 | 27-Apr-15 | 01-May-15 | 11 |
| CO-7148 | Final Inspection - Utilities | 5 | 5 | 27-Apr-15 | 01-May-15 | 11 |

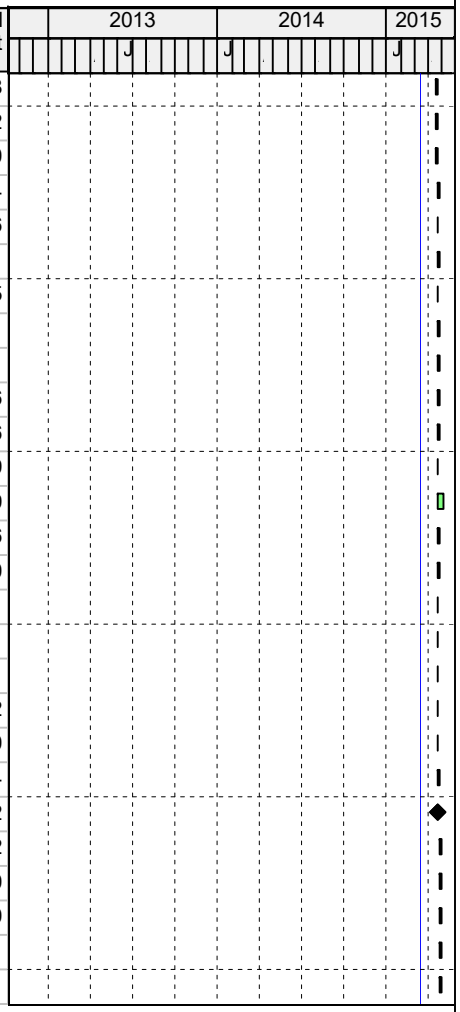



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8620 | Plumbing fixtures & trim at Pool | 2 | 2 | 28-Apr-15 | 29-Apr-15 | 0 |
| L03-8626 | Electrical trim & finish at Pool | 2 | 2 | 28-Apr-15 | 29-Apr-15 | 0 |
| L03-8628 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 28-Apr-15 | 29-Apr-15 | 0 |
| LL2-8150 | LL2 Floor Complete | 0 | 0 | | 29-Apr-15 | 8 |
| L03-8632 | Install restroom accessories at Pool | 2 | 2 | 30-Apr-15 | 01-May-15 | 0 |
| L03-8676 | Contractor Punchlist at Pool & Corridor (inspect/distrib | 3 | 3 | 04-May-15 | 06-May-15 | 0 |
| L03-8646 | Health inspection | 1 | 1 | 05-May-15 | 05-May-15 | 9 |
| CO-7500 | Complete Final Walsh/WPM Inspections/Corrections | 10 | 10 | 05-May-15 | 18-May-15 | 0 |
| L03-8678 | Owner Punchlist at Pool & Corridor (inspect/distribute/ | 2 | 2 | 07-May-15 | 08-May-15 | 0 |
| CM-1022 | Podium - "Clean/Punch" Complete - All Floors, All Zon | 0 | 0 | | 07-May-15 | 9 |
| L03-8680 | Final Cleaning at Pool & Corridor | 2 | 2 | 08-May-15 | 11-May-15 | 0 |
| CO-7124 | Final Inspection - Building Department | 2 | 2 | 19-May-15 | 20-May-15 | 0 |
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13 A | | |
| CM-1002 | CM - Contract Time (578 Cal Days) | 576 | 0 | 06-Mar-13 A | 05-Oct-14 A | |
| CM-1014 | CM - Start of Construction | 0 | 0 | 05-Apr-13 A | | |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 09-Mar-15 A | | |
| CM-1016 | CM - Owner FF+E "Build-Out" - Floors 4 & 5 | 7 | 0 | 09-Mar-15 A | 15-Mar-15 A | |
| CM-1006 | Construction Documents Issued by Client - (Due on 7 | 0 | 0 | 16-Mar-15 | | 66 |
| CM-1008 | Finalization of Allowances - (Due on 9-2-13) | 0 | 0 | 16-Mar-15 | | 66 |
| CO-7004 | CO - Prep / Submit O&M Manuals | 30 | 30 | 04-Apr-15 | 03-May-15 | 17 |
| CM-1018 | CM - Hotel Operations Training | 21 | 21 | 13-Apr-15 | 03-May-15 | 17 |
| CO-7006 | CO - Certificate of Occupancy/Substantial Completior | 0 | 0 | | 20-May-15 | 0 |
| CO-7122 | CO - Certificate of Occupancy | 0 | 0 | | 20-May-15 | 0 |

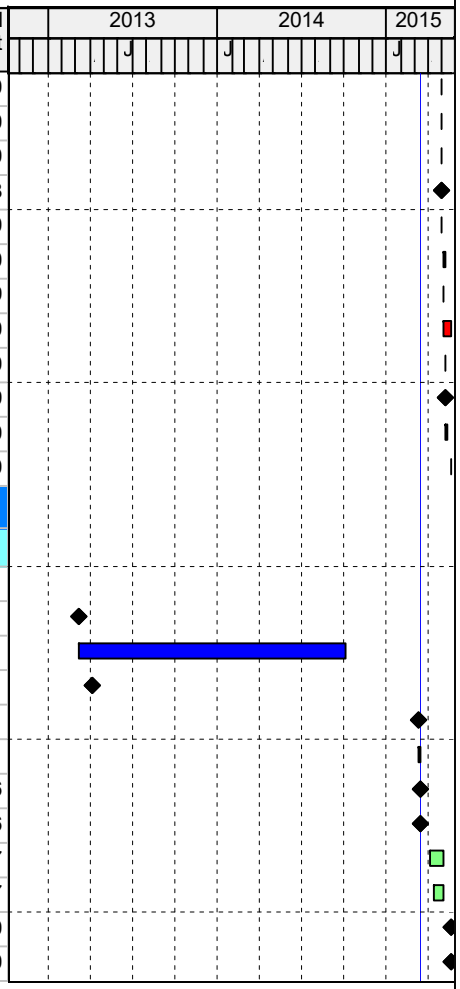



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Misc Milestones** | | | | | | |
| CM-1020 | MM - Site Mobilization | 10 | 0 | 06-Mar-13 A | 04-Apr-13 A | |
| MM-1008 | MM - Top Out - Tower / Structure | 0 | 0 | | 16-Apr-14 A | |
| MM-1004 | MM - Start Drywall In Tower | 0 | 0 | 27-Jun-14 A | | |
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 06-Sep-14 A | |
| MM-1010 | Energize Permanent Power | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| Tower Crane | | | | | | |
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 0 | 04-Jun-13 A | 14-Jun-13 A | |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 0 | 20-Jun-13 A | 24-Jun-13 A | |
| TC-5902 | Tower Crane - Erectiion | 2 | 0 | 21-Jun-13 A | 24-Jun-13 A | |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 24-Jun-13 A | | |
| TC-5906 | Tower Crane - Operatational Period | 391 | 0 | 24-Jun-13 A | 16-Jun-14 A | |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 0 | 16-Jun-14 A | 17-Jun-14 A | |
| Man & Material Lifts | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 0 | 14-Jan-14 A | 20-Jan-14 A | |
| ML-5952 | Man/Material Lifts - Erect/Build Loading Dock | 5 | 0 | 21-Jan-14 A | 27-Jan-14 A | |
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 10-Feb-14 A | | |
| ML-5954 | Man/Material Lifts - Load Test / Certify | 1 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| ML-5958 | Man/Material Lifts - Operatational Period | 196 | 0 | 10-Feb-14 A | 15-Nov-14 A | |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 2 | 0 | 15-Nov-14 A | 16-Nov-14 A | |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |
| Mass Excavation / Shoring | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 0 | 05-Apr-13 A | 12-Apr-13 A | |
| SW-2002 | Demolition And Utility Relocation | 8 | 0 | 15-Apr-13 A | 19-Apr-13 A | |

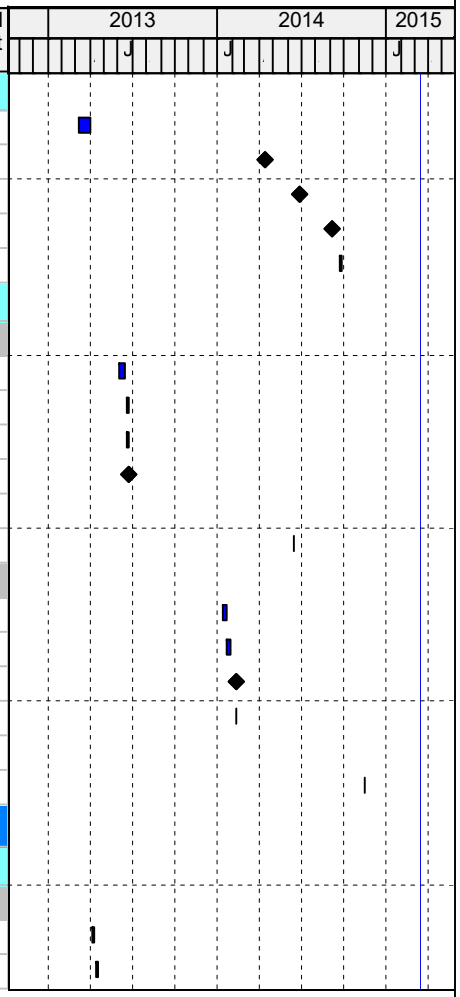



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2010 | Grade Subgrade for Elect/Plumbing | 3 | 0 | 07-Jan-14 A | 09-Jan-14 A | |
| **Site Finishes** | | | | | | |
| SW-2006 | Install Perm Power Electrical Service / Dry Utilities (Ofl | 15 | 0 | 20-May-14 A | 05-Jun-14 A | |
| SW-2004 | Offsite Water & Water Connection | 9 | 0 | 22-Sep-14 A | 01-Oct-14 A | |
| SW-2008 | Zone 4 - Landscaping & irrigation | 10 | 10 | 30-Mar-15 | 10-Apr-15 | 21 |
| **Structure** | | | | | | |
| **Foundation / Substructure - (Levels LL4 / LL3)** | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 0 | 12-Jun-13 A | 27-Jun-13 A | |
| LL4-1601 | LL4 - Excavate Footings | 14 | 0 | 17-Jun-13 A | 30-Jul-13 A | |
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 0 | 18-Jun-13 A | 24-Jun-13 A | |
| LL4-1606 | LL4 - Undrgmd Plumbing | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-1608 | LL4 - Undrgmd Elec | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 0 | 19-Jun-13 A | 25-Jun-13 A | |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 0 | 26-Jun-13 A | 02-Aug-13 A | |
| LL4-2033 | LL4 - Shotcrete Walls | 27 | 0 | 26-Jun-13 A | 05-Aug-13 A | |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 0 | 03-Jul-13 A | 21-Aug-13 A | |
| LL4-1614 | LL4 - FRP SOG | 5 | 0 | 10-Jul-13 A | 07-Aug-13 A | |
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 0 | 12-Jul-13 A | 26-Jul-13 A | |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 0 | 13-Jul-13 A | 06-Aug-13 A | |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 0 | 22-Jul-13 A | 24-Jul-13 A | |
| LL4-1618 | LL4 - FRP Ramp SOG | 5 | 0 | 01-Aug-13 A | 07-Aug-13 A | |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2004 | LL2 - Shore / Form Deck | 8 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2006 | LL3 - M & E Inserts | 4 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2008 | LL3 - ReSteel / PT Cables | 6 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2010 | LL3 - Install Embeds | 2 | 0 | 05-Aug-13 A | 09-Aug-13 A | |

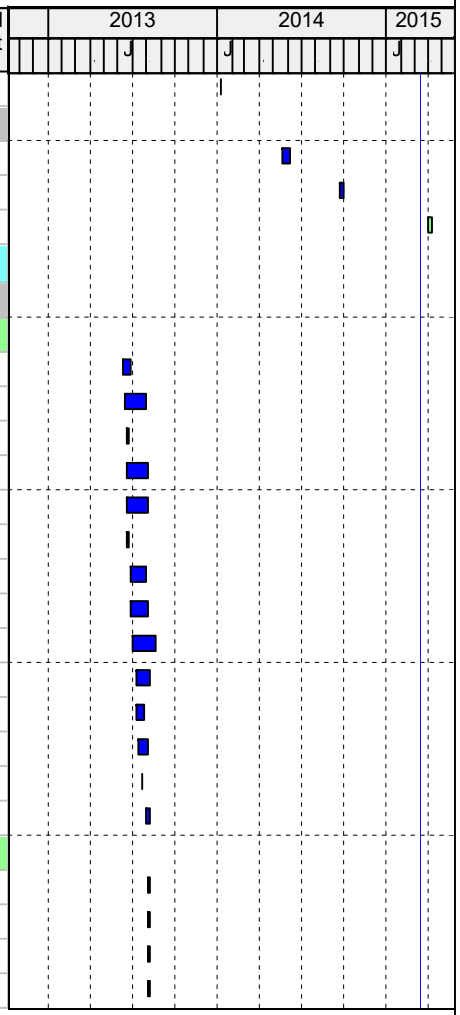


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-2001 | LL3 - Waterproof Walls | 3 | 0 | 05-Aug-13 A | 05-Aug-13 A | |
| LL3-2012 | LL3 - Pour / Finish Deck | 2 | 0 | 16-Aug-13 A | 16-Aug-13 A | |
| LL3-2014 | LL3 - Stress Tendons | 1 | 0 | 19-Aug-13 A | 19-Aug-13 A | |
| LL3-2000 | LL3 - FRP Core Walls | 8 | 0 | 19-Aug-13 A | 28-Aug-13 A | |
| LL3-2033 | LL3 - Shotcrete Walls | 5 | 0 | 23-Aug-13 A | 26-Aug-13 A | |
| LL3-2016 | LL3 - Strip / ReShore Deck | 3 | 0 | 01-Sep-13 A | 13-Sep-13 A | |
| LL3-2018 | LL3 - Remove ReShores | 4 | 0 | 04-Nov-13 A | 07-Nov-13 A | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Grids 1 to 4 - (SOG @ Loading Dock)** | | | | | | |
| LL2-2056 | LL2 - Grease Intercepter | 5 | 0 | 15-Aug-13 A | 21-Aug-13 A | |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 0 | 27-Aug-13 A | 04-Sep-13 A | |
| LL2-2027 | LL2 - Waterproof Walls | 2 | 0 | 27-Aug-13 A | 28-Aug-13 A | |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 0 | 30-Aug-13 A | 05-Sep-13 A | |
| LL2-2021 | LL2 - FRP Elec Vault | 14 | 0 | 30-Aug-13 A | 04-Sep-13 A | |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 0 | 04-Sep-13 A | 11-Sep-13 A | |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 0 | 11-Sep-13 A | 13-Sep-13 A | |
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls/Roof | 11 | 0 | 19-Sep-13 A | 03-Oct-13 A | |
| LL2-2020 | LL2 - Undrgmd Plumbing | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2022 | LL2 - Undrgmd Elec | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2031 | LL2 - FRP Generator SOG | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2015 | LL2 to LL1 FRP Columns / Misc Walls | 6 | 0 | 01-Oct-13 A | 01-Oct-13 A | |
| LL2-2029 | LL2 - F/R/P Pour #2 | 8 | 0 | 15-Jan-14 A | 24-Jan-14 A | |
| LL2-2011 | LL2 - F/R/P Pour #3 | 16 | 0 | 24-Jan-14 A | 18-Feb-14 A | |
| LL2-2019 | LL2 - F/R/P Pour #6 | 4 | 0 | 19-Feb-14 A | 17-Mar-14 A | |
| LL2-2044 | LL2 - Set Generator | 1 | 0 | 16-May-14 A | 16-May-14 A | |

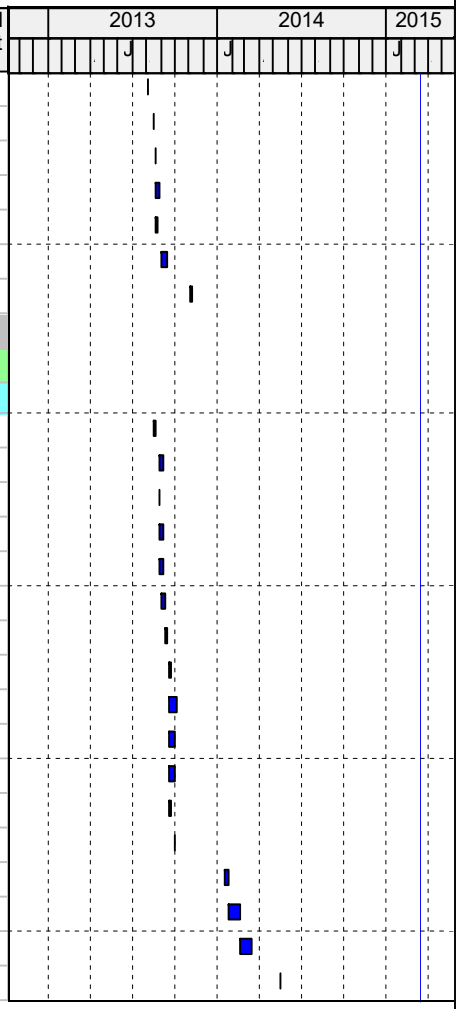



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |
| LL2-2004 | LL2 - Shore / Form Deck | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2035 | LL2 to LL1 - Shotcrete Walls | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2006 | LL2 - M & E Inserts | 4 | 0 | 14-Aug-13 A | 19-Aug-13 A | |
| LL2-2008 | LL2 - ReSteel / PT Cables | 6 | 0 | 14-Aug-13 A | 21-Aug-13 A | |
| LL2-2010 | LL2 - Install Embeds | 3 | 0 | 14-Aug-13 A | 16-Aug-13 A | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 0 | 27-Aug-13 A | 06-Sep-13 A | |
| LL2-2012 | LL2 - Place / Finish Deck | 3 | 0 | 29-Aug-13 A | 29-Aug-13 A | |
| LL2-2023 | LL2 - Waterproof Walls | 3 | 0 | 29-Aug-13 A | 03-Sep-13 A | |
| LL2-2014 | LL2 - Stress Tendons | 1 | 0 | 30-Aug-13 A | 30-Aug-13 A | |
| LL2-2016 | LL2 - Strip / ReShore | 3 | 0 | 03-Sep-13 A | 05-Sep-13 A | |
| LL2-8234 | LL2 - Place / Finish Deck | 3 | 0 | 12-Sep-13 A | 12-Sep-13 A | |
| LL2-2000 | LL2 - FRP Core Walls | 8 | 0 | 12-Sep-13 A | 23-Sep-13 A | |
| LL2-2018 | LL2 - Remove ReShores | 4 | 0 | 13-Nov-13 A | 18-Nov-13 A | |
| LL2-2013 | LL2 - F/R/P Pour #1 | 4 | 0 | 13-Jan-14 A | 16-Jan-14 A | |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| P5A-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2000 | LL1 - FRP Core Walls | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2004 | LL1 - Shore / Form Deck | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| P6-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P6-2004 | LL1 - Shore / Form Deck | 7 | 0 | 16-Sep-13 A | 24-Sep-13 A | |
| P5A-2006 | LL1 - MEP Rough In | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2008 | LL1 - ReSteel / PT Cables | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2012 | LL1 - Place / Finish Deck | 0 | 0 | 20-Sep-13 A | | |
| P5A-2020 | LL1 - Waterproof Walls | 3 | 0 | 20-Sep-13 A | 24-Sep-13 A | |
| P5A-2014 | LL1 - Stress Tendons | 1 | 0 | 23-Sep-13 A | 23-Sep-13 A | |

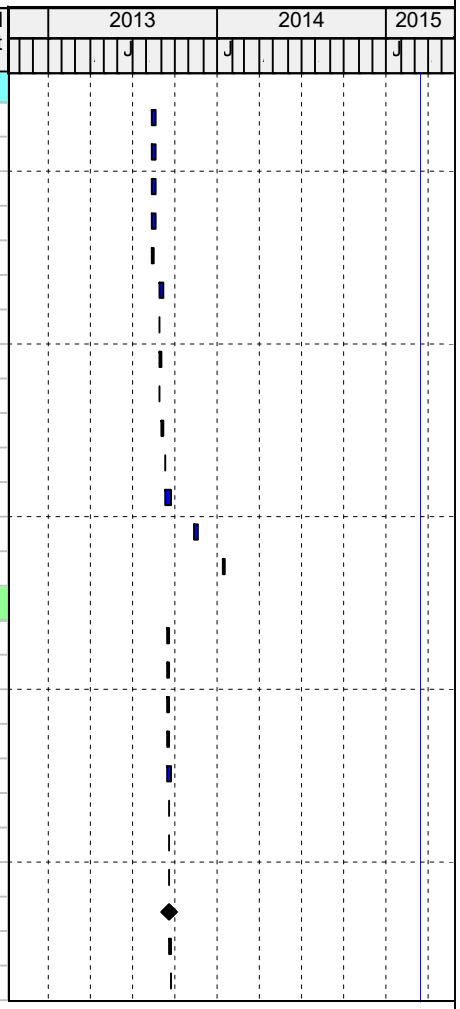



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P5A-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2006 | LL1 - MEP Rough In | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2008 | LL1 - ReSteel / PT Cables | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 24-Sep-13 A | 25-Sep-13 A | |
| P6-2020 | LL1 - Waterproof Walls | 4 | 0 | 24-Sep-13 A | 27-Sep-13 A | |
| P5A-2033 | LL1 - Resteel/Shotcrete Walls | 3 | 0 | 25-Sep-13 A | 27-Sep-13 A | |
| P5B-2002 | LL1 - FRP Columns Below | 5 | 0 | 26-Sep-13 A | 02-Oct-13 A | |
| P5B-2004 | LL1 - Shore / Form Deck | 7 | 0 | 26-Sep-13 A | 04-Oct-13 A | |
| P6-2012 | LL1 - Place / Finish Deck | 0 | 0 | 27-Sep-13 A | | |
| P6-2014 | LL1 - Stress Tendons | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2033 | LL1 - Resteel/Shotcrete Walls | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 01-Oct-13 A | 03-Oct-13 A | |
| P5B-2006 | LL1 - MEP Rough In | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2002 | FRP Columns Below | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2004 | Shore / Form Deck | 4 | 0 | 03-Oct-13 A | 08-Oct-13 A | |
| P5B-2008 | LL1 - ReSteel / PT Cables | 5 | 0 | 04-Oct-13 A | 10-Oct-13 A | |
| P5B-2010 | LL1 - Install Edgeform/Embeds | 4 | 0 | 04-Oct-13 A | 09-Oct-13 A | |
| P8-2002 | FRP Columns Below | 5 | 0 | 07-Oct-13 A | 11-Oct-13 A | |
| P8-2000 | Form/Resteel/Close Core Walls | 14 | 0 | 07-Oct-13 A | 24-Oct-13 A | |
| P8-2004 | Shore / Form Deck P8 | 8 | 0 | 07-Oct-13 A | 16-Oct-13 A | |
| P7-2002 | FRP Columns Below | 5 | 0 | 08-Oct-13 A | 14-Oct-13 A | |
| P7-2004 | Shore / Form Deck | 6 | 0 | 08-Oct-13 A | 15-Oct-13 A | |
| P10A--2006 | MEP Rough In | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2008 | ReSteel / PT Cables | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2010 | Install Edgeform/Embeds | 2 | 0 | 08-Oct-13 A | 09-Oct-13 A | |
| P5B-2012 | LL1 - Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P10A--2012 | Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |

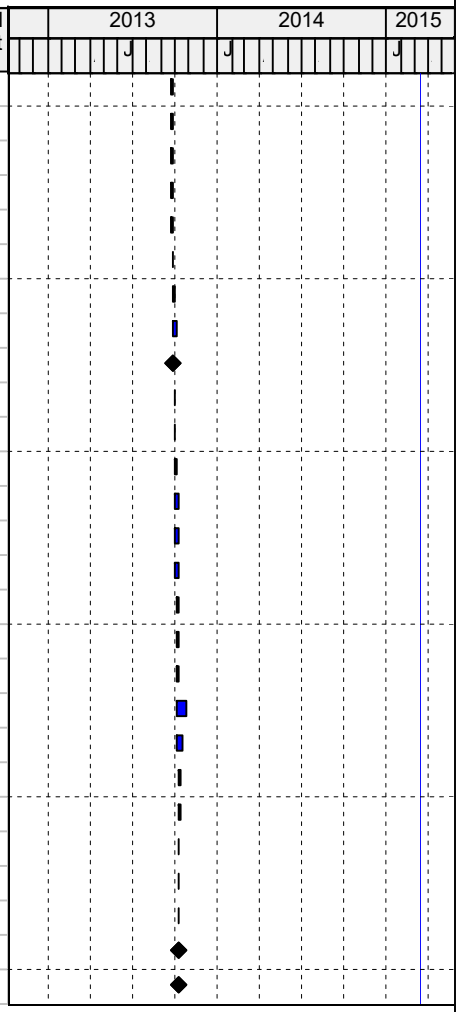



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P5B-2014 | LL1 - Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P7-2006 | MEP Rough In | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P7-2008 | ReSteel / PT Cables | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P10A--2014 | Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P8-2020 | Shore / Form Deck P9 | 6 | 0 | 14-Oct-13 A | 21-Oct-13 A | |
| P5B-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2010 | Install Edgeform/Embeds | 2 | 0 | 15-Oct-13 A | 16-Oct-13 A | |
| P8-2006 | MEP Rough In | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2008 | ReSteel / PT Cables | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2010 | Install Edgeform/Embeds | 4 | 0 | 15-Oct-13 A | 18-Oct-13 A | |
| P10A--2016 | Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2012 | Place / Finish Deck | 0 | 0 | 18-Oct-13 A | | |
| P7-2033 | Resteel/Shotcrete Walls | 3 | 0 | 18-Oct-13 A | 22-Oct-13 A | |
| P7-2014 | Stress Tendons | 1 | 0 | 21-Oct-13 A | 21-Oct-13 A | |
| P7-2016 | Strip / ReShore Deck | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2002 | FRP Columns Below | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P10B--2000 | FRP Shear Walls Below | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2004 | Shore / Form Deck | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P8-2012 | Place / Finish Deck P 8 & 9 and Core Walls | 0 | 0 | 25-Oct-13 A | | |
| P8-2014 | Stress Tendons | 1 | 0 | 28-Oct-13 A | 28-Oct-13 A | |
| P10B--2006 | MEP Rough In | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2008 | ReSteel / PT Cables | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2010 | Install Edgeform/Embeds | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P12--2002 | FRP Columns Below | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P12--2000 | Form/Resteel/Close Core Walls | 9 | 0 | 28-Oct-13 A | 07-Nov-13 A | |
| P12--2004 | Shore / Form Deck | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P8-2016 | Strip / ReShore Deck | 3 | 0 | 29-Oct-13 A | 31-Oct-13 A | |

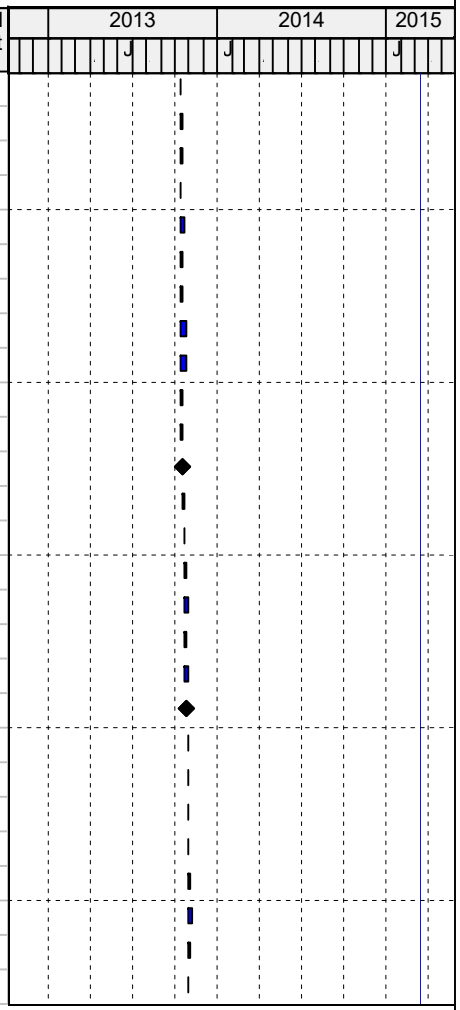



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P11–2002 | FRP Columns Below | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P11–2004 | Shore / Form Deck | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P10B–2012 | Place / Finish Deck | 0 | 0 | 31-Oct-13 A | | |
| P10B–2014 | Stress Tendons | 1 | 0 | 01-Nov-13 A | 01-Nov-13 A | |
| P12–2006 | MEP Rough In | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12–2008 | ReSteel / PT Cables | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12–2010 | Install Edgeform/Embeds | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P10B–2016 | Strip / ReShore Deck | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2006 | MEP Rough In | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2008 | ReSteel / PT Cables | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2010 | Install Edgeform/Embeds | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2012 | Place / Finish Deck | 0 | 0 | 07-Nov-13 A | | |
| P13–2002 | FRP Columns Below | 5 | 0 | 07-Nov-13 A | 14-Nov-13 A | |
| P13–2004 | Shore / Form Deck | 9 | 0 | 07-Nov-13 A | 28-Nov-13 A | |
| P11–2014 | Stress Tendons | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| P12–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 08-Nov-13 A | | |
| P11–2016 | Strip / ReShore Deck | 3 | 0 | 12-Nov-13 A | 14-Nov-13 A | |
| P12–2014 | Stress Tendons | 1 | 0 | 12-Nov-13 A | 12-Nov-13 A | |
| P14–2002 | FRP Columns Below | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P14–2000 | Form/Resteel/Close Core Walls | 8 | 0 | 19-Nov-13 A | 03-Dec-13 A | |
| P14–2004 | Shore / Form Deck | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P13A–2002 | FRP Columns Below | 5 | 0 | 21-Nov-13 A | 27-Nov-13 A | |
| P13A–2004 | Shore / Form Deck | 4 | 0 | 21-Nov-13 A | 26-Nov-13 A | |
| P13–2010 | Install Edgeform/Embeds | 5 | 0 | 22-Nov-13 A | 04-Dec-13 A | |
| P13–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2006 | MEP Rough In | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |

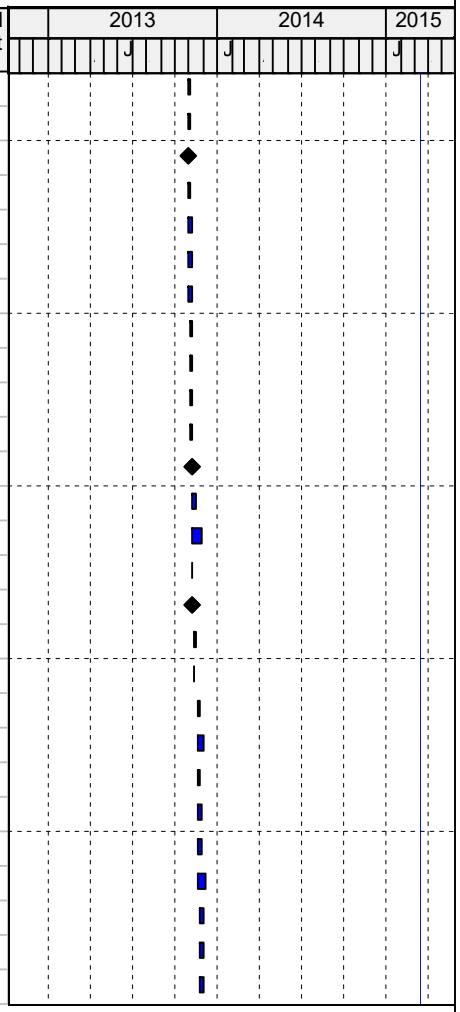


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P14–2010 | Install Edgeform/Embeds | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P13–2006 | MEP Rough In | 5 | 0 | 26-Nov-13 A | 03-Dec-13 A | |
| P13A–2006 | MEP Rough In | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2008 | ReSteel / PT Cables | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2010 | Install Edgeform/Embeds | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13–2012 | Place / Finish Deck | 0 | 0 | 02-Dec-13 A | | |
| P13A–2012 | Place / Finish Deck | 0 | 0 | 03-Dec-13 A | | |
| P14–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 04-Dec-13 A | | |
| P13–2014 | Stress Tendons | 1 | 0 | 05-Dec-13 A | 05-Dec-13 A | |
| P15–2002 | FRP Columns Below | 3 | 0 | 05-Dec-13 A | 09-Dec-13 A | |
| P15–2000 | Jump/Resteel/Close Core | 9 | 0 | 05-Dec-13 A | 17-Dec-13 A | |
| P15–2004 | Shore / Form Deck | 5 | 0 | 05-Dec-13 A | 11-Dec-13 A | |
| P13–2016 | Strip / ReShore Deck | 3 | 0 | 06-Dec-13 A | 10-Dec-13 A | |
| P13A–2014 | Stress Tendons | 1 | 0 | 06-Dec-13 A | 06-Dec-13 A | |
| P14–2014 | Stress Tendons | 1 | 0 | 07-Dec-13 A | 07-Dec-13 A | |
| P15–2006 | MEP Rough In | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2008 | ReSteel / PT Cables | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2010 | Install Edgeform/Embeds | 3 | 0 | 11-Dec-13 A | 13-Dec-13 A | |
| P16-2002 | FRP Columns Below | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P16-2004 | Shore / Form Deck | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P15–2012 | Place / Finish Deck | 0 | 0 | 18-Dec-13 A | | |
| P15–2020 | Place Conc @ Core | 0 | 0 | 18-Dec-13 A | | |
| P16-2000 | Jump/Resteel/Close Core | 5 | 0 | 18-Dec-13 A | 24-Dec-13 A | |
| P16-2006 | MEP Rough In | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2008 | ReSteel / PT Cables | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2010 | Install Edgeform/Embeds | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P15–2014 | Stress Tendons | 1 | 0 | 21-Dec-13 A | 21-Dec-13 A | |

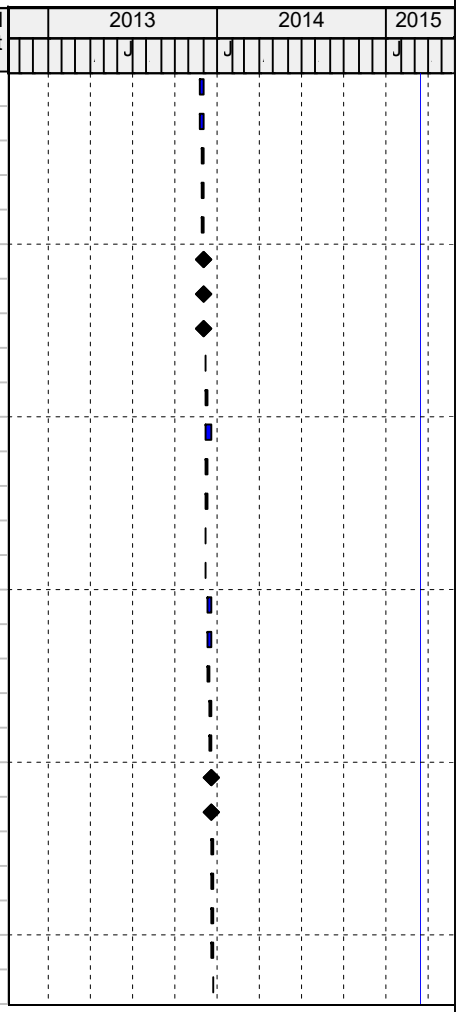


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P8-2018 | Remove Reshores | 2 | 0 | 23-Dec-13 A | 24-Dec-13 A | |
| P10A–2018 | Remove Reshores | 2 | 0 | 26-Dec-13 A | 27-Dec-13 A | |
| P16-2012 | Place / Finish Deck | 0 | 0 | 26-Dec-13 A | | |
| P16-2020 | Place Conc @ Core | 0 | 0 | 26-Dec-13 A | | |
| P17-2002 | FRP Columns Below | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P17-2000 | Jump/Resteel/Close Core | 7 | 0 | 27-Dec-13 A | 07-Jan-14 A | |
| P17-2004 | Shore / Form Deck | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P10B–2018 | Remove Reshores | 2 | 0 | 30-Dec-13 A | 31-Dec-13 A | |
| P16-2014 | Stress Tendons | 1 | 0 | 31-Dec-13 A | 31-Dec-13 A | |
| P5A-2018 | LL1 - Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P11–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P12–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P17-2006 | MEP Rough In | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2008 | ReSteel / PT Cables | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2010 | Install Edgeform/Embeds | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P6-2018 | LL1 - Remove Reshores | 2 | 0 | 06-Jan-14 A | 07-Jan-14 A | |
| P5B-2018 | LL1 - Remove Reshores | 2 | 0 | 08-Jan-14 A | 09-Jan-14 A | |
| P17-2012 | Place / Finish Deck | 0 | 0 | 08-Jan-14 A | | |
| P17-2020 | Place Conc @ Core | 0 | 0 | 08-Jan-14 A | | |
| P18-2002 | FRP Columns Below | 5 | 0 | 09-Jan-14 A | 15-Jan-14 A | |
| P18-2000 | Jump/Resteel/Close Core | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P18-2004 | Shore / Form Deck | 3 | 0 | 09-Jan-14 A | 13-Jan-14 A | |
| LL2-2022R | MEP Rough In | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P7-2018 | Remove Reshores | 2 | 0 | 10-Jan-14 A | 13-Jan-14 A | |
| P17-2014 | Stress Tendons | 1 | 0 | 11-Jan-14 A | 11-Jan-14 A | |
| P13–2018 | Remove Reshores | 2 | 0 | 13-Jan-14 A | 14-Jan-14 A | |
| P13A–2018 | Remove Reshores | 2 | 0 | 15-Jan-14 A | 16-Jan-14 A | |

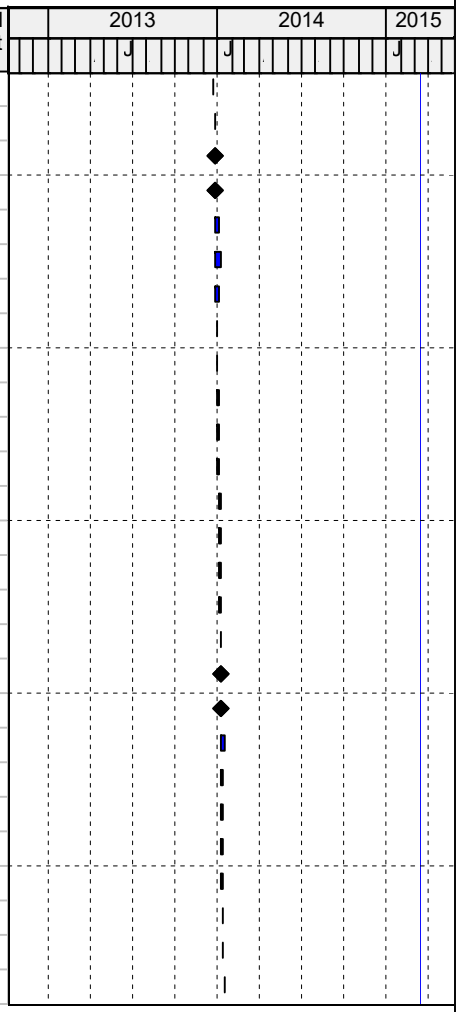


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| WEA-2012 | WIND IMPACT | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| P18-2006 | MEP Rough In | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2008 | ReSteel / PT Cables | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2010 | Install Edgeform/Embeds | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2012 | Place / Finish Deck | 0 | 0 | 22-Jan-14 A | | |
| P18-2020 | Place Conc @ Core | 0 | 0 | 22-Jan-14 A | | |
| P19-2002 | FRP Columns Below | 5 | 0 | 23-Jan-14 A | 29-Jan-14 A | |
| P19-2000 | Jump/Resteel/Close Core | 4 | 0 | 23-Jan-14 A | 28-Jan-14 A | |
| P19-2004 | Shore / Form Deck | 3 | 0 | 23-Jan-14 A | 27-Jan-14 A | |
| P18-2014 | Stress Tendons | 1 | 0 | 25-Jan-14 A | 25-Jan-14 A | |
| P14–2018 | Remove Reshores | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2006 | MEP Rough In | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2008 | ReSteel / PT Cables | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2010 | Install Edgeform/Embeds | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2012 | Place / Finish Deck | 0 | 0 | 29-Jan-14 A | | |
| P19-2020 | Place Conc @ Core | 0 | 0 | 29-Jan-14 A | | |
| P20-2002 | FRP Columns Below | 5 | 0 | 30-Jan-14 A | 05-Feb-14 A | |
| P20-2000 | Jump/Resteel/Close Core | 9 | 0 | 30-Jan-14 A | 11-Feb-14 A | |
| P20-2004 | Shore / Form Deck | 6 | 0 | 30-Jan-14 A | 10-Feb-14 A | |
| P19-2014 | Stress Tendons | 1 | 0 | 01-Feb-14 A | 01-Feb-14 A | |
| P13A–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P14–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P15–2016 | Strip / ReShore Deck | 3 | 0 | 06-Feb-14 A | 10-Feb-14 A | |
| P20-2006 | MEP Rough In | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2008 | ReSteel / PT Cables | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2010 | Install Edgeform/Embeds | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| L03-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 06-Feb-14 A | 12-Feb-14 A | |

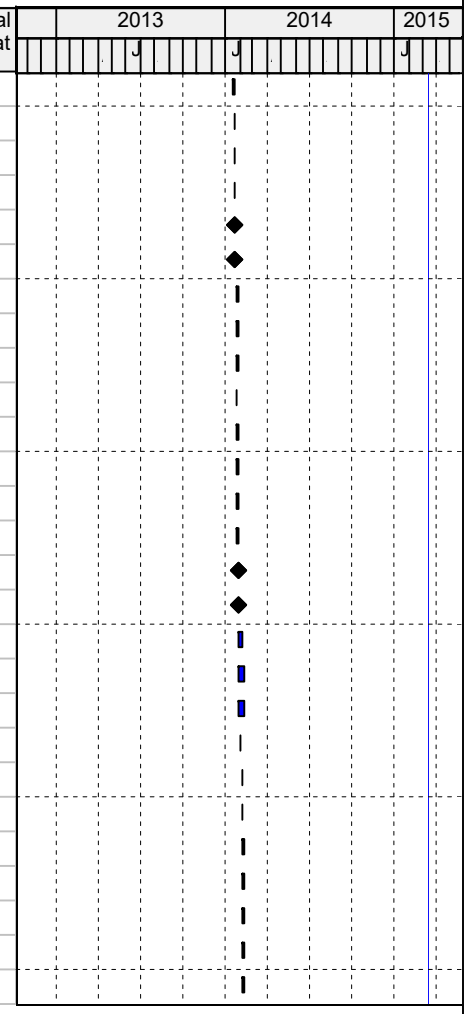


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P16-2016 | Strip / ReShore Deck | 3 | 0 | 10-Feb-14 A | 12-Feb-14 A | |
| L04-2018 | Remove Reshores | 2 | 0 | 10-Feb-14 A | 11-Feb-14 A | |
| L03-2018 | Remove Reshores | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| P17-2016 | Strip / ReShore Deck | 3 | 0 | 12-Feb-14 A | 14-Feb-14 A | |
| P20-2012 | Place / Finish Deck | 0 | 0 | 12-Feb-14 A | | |
| P20-2020 | Place Conc @ Core | 0 | 0 | 12-Feb-14 A | | |
| L04-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-Feb-14 A | 18-Feb-14 A | |
| P12–2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P18-2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P21-2002 | FRP Columns Below | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| P21-2000 | Jump/Resteel/Close Core | 4 | 0 | 13-Feb-14 A | 18-Feb-14 A | |
| P21-2004 | Shore / Form Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P19-2016 | Strip / ReShore Deck | 3 | 0 | 14-Feb-14 A | 18-Feb-14 A | |
| P20-2014 | Stress Tendons | 1 | 0 | 15-Feb-14 A | 15-Feb-14 A | |
| P21-2006 | MEP Rough In | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2008 | ReSteel / PT Cables | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P20-2016 | Strip / ReShore Deck | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| L05-2018 | Remove Reshores | 2 | 0 | 18-Feb-14 A | 19-Feb-14 A | |
| P21-2012 | Place / Finish Deck | 0 | 0 | 19-Feb-14 A | | |
| P21-2020 | Place Conc @ Core | 0 | 0 | 19-Feb-14 A | | |
| P22-2002 | FRP Columns Below | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P22-2000 | Jump/Resteel/Close Core | 4 | 0 | 20-Feb-14 A | 25-Feb-14 A | |
| P22-2004 | Shore / Form Deck | 3 | 0 | 20-Feb-14 A | 24-Feb-14 A | |
| L05-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P21-2014 | Stress Tendons | 1 | 0 | 22-Feb-14 A | 22-Feb-14 A | |
| P21-2016 | Strip / ReShore Deck | 3 | 0 | 24-Feb-14 A | 26-Feb-14 A | |

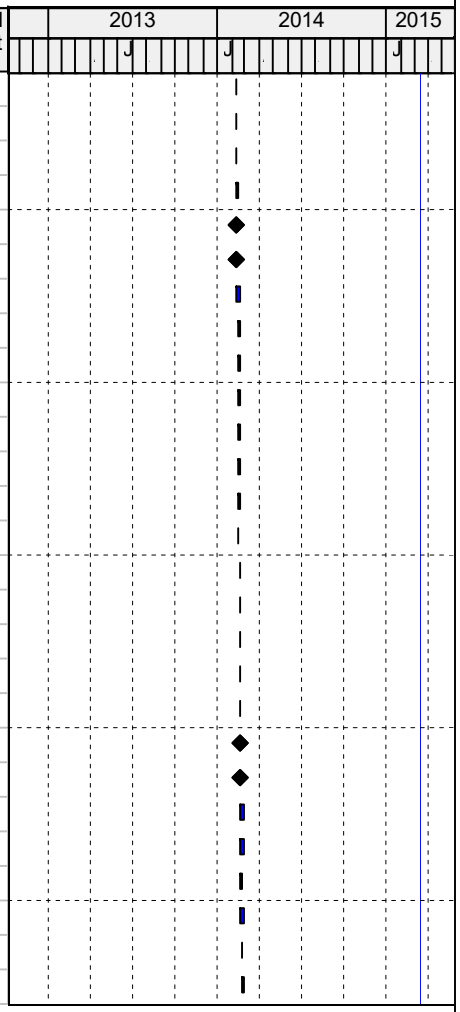



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P22-2006 | MEP Rough In | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2008 | ReSteel / PT Cables | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| L06-2018 | Remove Reshores | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| P22-2012 | Place / Finish Deck | 0 | 0 | 26-Feb-14 A | | |
| P22-2020 | Place Conc @ Core | 0 | 0 | 26-Feb-14 A | | |
| P23-2002 | FRP Columns Below | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2000 | Jump/Resteel/Close Core | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2004 | Shore / Form Deck | 3 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2006 | MEP Rough In | 2 | 0 | 01-Mar-14 A | 03-Mar-14 A | |
| P22-2014 | Stress Tendons | 1 | 0 | 01-Mar-14 A | 01-Mar-14 A | |
| P23-2008 | ReSteel / PT Cables | 2 | 0 | 03-Mar-14 A | 04-Mar-14 A | |
| P22-2016 | Strip / ReShore Deck | 3 | 0 | 04-Mar-14 A | 10-Mar-14 A | |
| P23-2010 | Install Edgeform/Embeds | 2 | 0 | 04-Mar-14 A | 04-Mar-14 A | |
| L07-2018 | Remove Reshores | 2 | 0 | 04-Mar-14 A | 05-Mar-14 A | |
| P23-2012 | Place / Finish Deck | 0 | 0 | 05-Mar-14 A | | |
| P23-2020 | Place Conc @ Core | 0 | 0 | 05-Mar-14 A | | |
| P24-2002 | FRP Columns Below | 5 | 0 | 05-Mar-14 A | 07-Mar-14 A | |
| P24-2004 | Shore / Form Deck | 3 | 0 | 06-Mar-14 A | 10-Mar-14 A | |
| P24-2000 | Jump/Resteel/Close Core | 4 | 0 | 08-Mar-14 A | 10-Mar-14 A | |
| P23-2014 | Stress Tendons | 1 | 0 | 10-Mar-14 A | 10-Mar-14 A | |
| P24-2008 | ReSteel / PT Cables | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P24-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P23-2016 | Strip / ReShore Deck | 3 | 0 | 11-Mar-14 A | 17-Mar-14 A | |
| P24-2006 | MEP Rough In | 2 | 0 | 11-Mar-14 A | 11-Mar-14 A | |
| P25-2002 | FRP Columns Below | 5 | 0 | 11-Mar-14 A | 13-Mar-14 A | |
| L08-2018 | Remove Reshores | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |

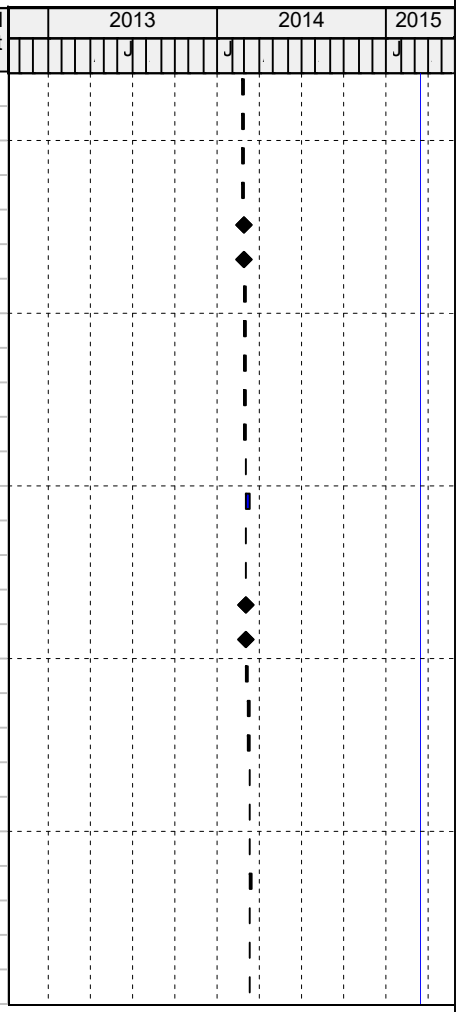



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P24-2012 | Place / Finish Deck | 0 | 0 | 12-Mar-14 A | | |
| P24-2020 | Place Conc @ Core | 0 | 0 | 12-Mar-14 A | | |
| P25-2004 | Shore / Form Deck | 3 | 0 | 13-Mar-14 A | 17-Mar-14 A | |
| P25-2000 | Jump/Resteel/Close Core | 4 | 0 | 15-Mar-14 A | 17-Mar-14 A | |
| P24-2014 | Stress Tendons | 1 | 0 | 17-Mar-14 A | 17-Mar-14 A | |
| P25-2006 | MEP Rough In | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2008 | ReSteel / PT Cables | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| L06-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 18-Mar-14 A | 20-Mar-14 A | |
| L09-2018 | Remove Reshores | 2 | 0 | 18-Mar-14 A | 19-Mar-14 A | |
| P26-2002 | FRP Columns Below | 5 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| P25-2012 | Place / Finish Deck | 0 | 0 | 19-Mar-14 A | | |
| P25-2020 | Place Conc @ Core | 0 | 0 | 19-Mar-14 A | | |
| P26-2004 | Shore / Form Deck | 3 | 0 | 20-Mar-14 A | 24-Mar-14 A | |
| L07-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 21-Mar-14 A | 25-Mar-14 A | |
| P26-2000 | Jump/Resteel/Close Core | 4 | 0 | 22-Mar-14 A | 24-Mar-14 A | |
| P26-2006 | MEP Rough In | 2 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P26-2008 | ReSteel / PT Cables | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P26-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P25-2014 | Stress Tendons | 1 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P27-2002 | FRP Columns Below | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| P26-2012 | Place / Finish Deck | 0 | 0 | 26-Mar-14 A | | |
| P26-2020 | Place Conc @ Core | 0 | 0 | 26-Mar-14 A | | |
| L08-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 26-Mar-14 A | 28-Mar-14 A | |
| L10-2018 | Remove Reshores | 2 | 0 | 26-Mar-14 A | 27-Mar-14 A | |
| P27-2004 | Shore / Form Deck | 3 | 0 | 27-Mar-14 A | 31-Mar-14 A | |
| P27-2000 | Jump/Resteel/Close Core | 4 | 0 | 29-Mar-14 A | 31-Mar-14 A | |

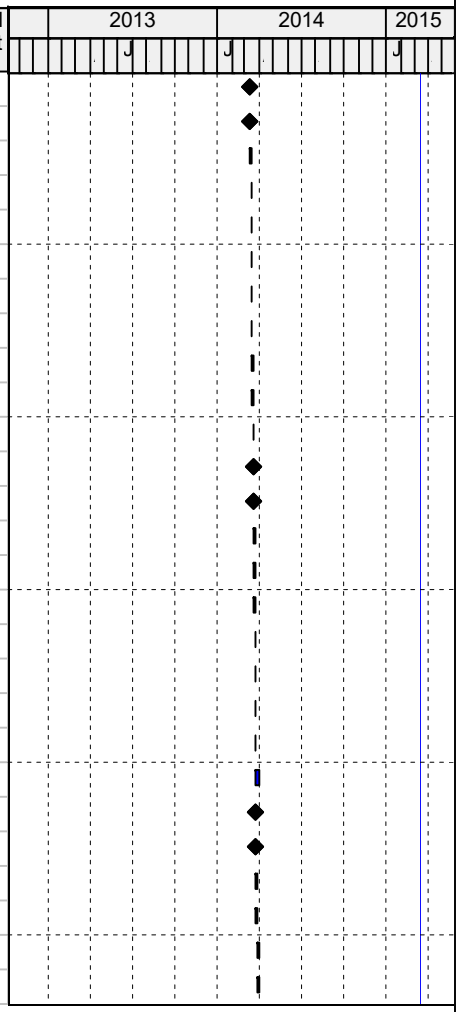



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P27-2006 | MEP Rough In | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2008 | ReSteel / PT Cables | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2010 | Install Edgeform/Embeds | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P26-2014 | Stress Tendons | 1 | 0 | 31-Mar-14 A | 31-Mar-14 A | |
| L09-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 31-Mar-14 A | 02-Apr-14 A | |
| P24-2016 | Strip / ReShore Deck | 3 | 0 | 01-Apr-14 A | 07-Apr-14 A | |
| L11-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 02-Apr-14 A | |
| L12-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 03-Apr-14 A | |
| P27-2012 | Place / Finish Deck | 0 | 0 | 02-Apr-14 A | | |
| P27-2020 | Place Conc @ Core | 0 | 0 | 02-Apr-14 A | | |
| P28-2002 | FRP Columns Below | 5 | 0 | 02-Apr-14 A | 04-Apr-14 A | |
| P28-2004 | Shore / Form Deck | 4 | 0 | 03-Apr-14 A | 08-Apr-14 A | |
| L10-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| P27-2014 | Stress Tendons | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| P25-2016 | Strip / ReShore Deck | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L14-2018 | Remove Reshores | 2 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| P28-2000 | Jump/Resteel/Close Core | 7 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| P28-2006 | MEP Rough In | 4 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2008 | ReSteel / PT Cables | 4 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Apr-14 A | 11-Apr-14 A | |
| L12-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| P28-2012 | Place / Finish Deck | 0 | 0 | 14-Apr-14 A | | |
| P28-2020 | Place Conc @ Core | 0 | 0 | 14-Apr-14 A | | |
| P29-2002 | FRP Columns Above Roof Deck | 3 | 0 | 14-Apr-14 A | 18-Apr-14 A | |
| P26-2016 | Strip / ReShore Deck | 3 | 0 | 14-Apr-14 A | 17-Apr-14 A | |
| L14-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-Apr-14 A | 18-Apr-14 A | |

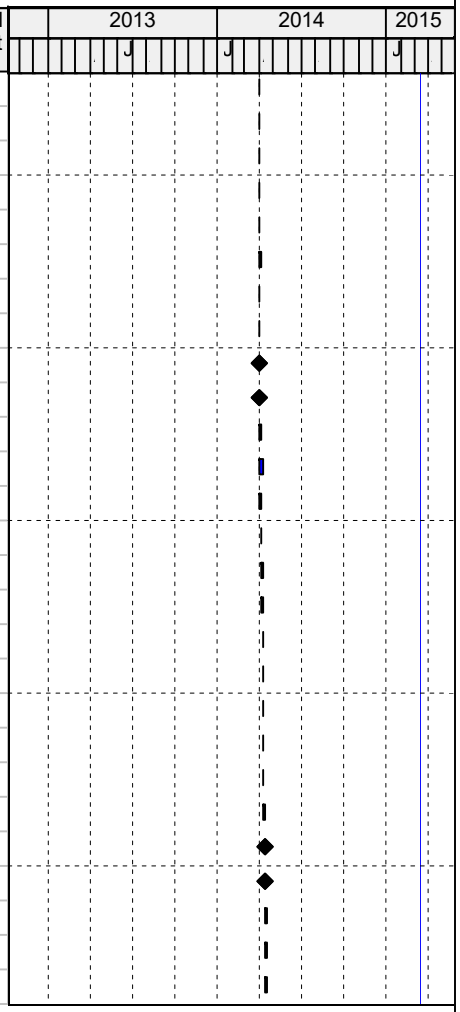



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P28-2014 | Stress Tendons | 1 | 0 | 17-Apr-14 A | 17-Apr-14 A | |
| P29-2000 | Strip Core | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| P27-2016 | Strip / ReShore Deck | 3 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L15-2018 | Remove Reshores | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| P28-2016 | Strip / ReShore Deck | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L15-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L16-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-May-14 A | 19-May-14 A | |
| L16-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2019 | Grind Ceiling for Skim Coat | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| **Ballroom Catwalk & Roof** | | | | | | |
| PC-2100 | Erect Structural Steel @ Porte Cochere | 3 | 0 | 30-Jan-14 A | 03-Feb-14 A | |
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 7 | 0 | 07-Feb-14 A | 17-Feb-14 A | |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| PC-2102 | Metal Decking @ Porte Cochere/ Roof | 2 | 0 | 17-Apr-14 A | 18-Apr-14 A | |
| BR-2112 | BR - Fireproofing @ Structural Steel | 2 | 0 | 27-May-14 A | 30-May-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Mech Penthouse** | | | | | | |
| PH-8706 | Set Mech Equipment @ Tower Roof | 3 | 0 | 22-May-14 A | 28-May-14 A | |
| PH-8708 | Set Equipment @ Penthouse | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| PH-8700 | PH - Structural Steel and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| **Vertical Circulation** | | | | | | |
| **Stairs** | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 25-Nov-13 A | 26-Nov-13 A | |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 27-Nov-13 A | 03-Dec-13 A | |
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 04-Dec-13 A | 05-Dec-13 A | |

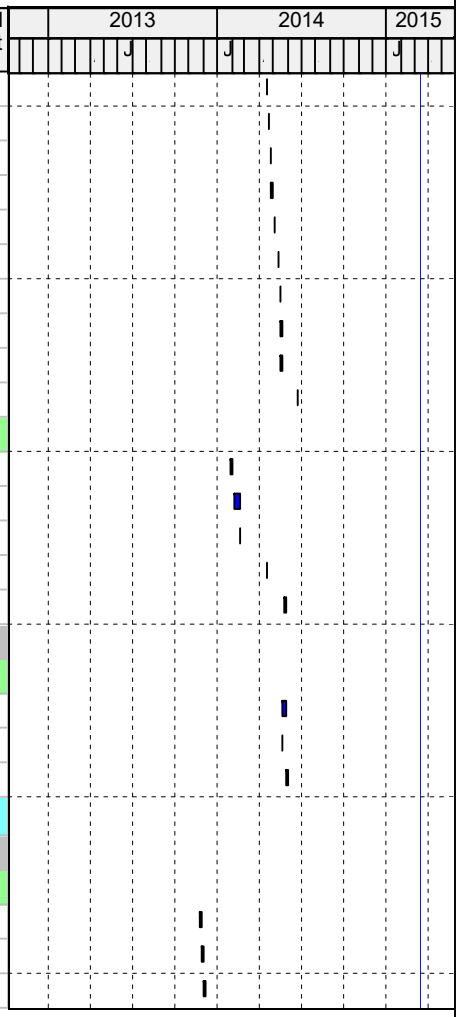



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 06-Dec-13 A | 09-Dec-13 A | |
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 2 | 0 | 03-Feb-14 A | 04-Feb-14 A | |
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 2 | 0 | 06-Feb-14 A | 07-Feb-14 A | |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 2 | 0 | 07-Feb-14 A | 07-Feb-14 A | |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 2 | 0 | 07-Feb-14 A | 10-Feb-14 A | |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 2 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 2 | 0 | 06-Mar-14 A | 07-Mar-14 A | |
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 2 | 0 | 07-Mar-14 A | 10-Mar-14 A | |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 2 | 0 | 13-Mar-14 A | 14-Mar-14 A | |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 2 | 0 | 08-Apr-14 A | 21-Apr-14 A | |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| S1-4040 | Stair 1 - Set Mtl Stairs / Railings L18 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 10-Dec-13 A | 11-Dec-13 A | |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 12-Dec-13 A | 13-Dec-13 A | |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 16-Dec-13 A | 17-Dec-13 A | |
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 18-Dec-13 A | 19-Dec-13 A | |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 2 | 0 | 12-Feb-14 A | 13-Feb-14 A | |
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 2 | 0 | 13-Feb-14 A | 13-Feb-14 A | |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 2 | 0 | 13-Feb-14 A | 14-Feb-14 A | |
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |

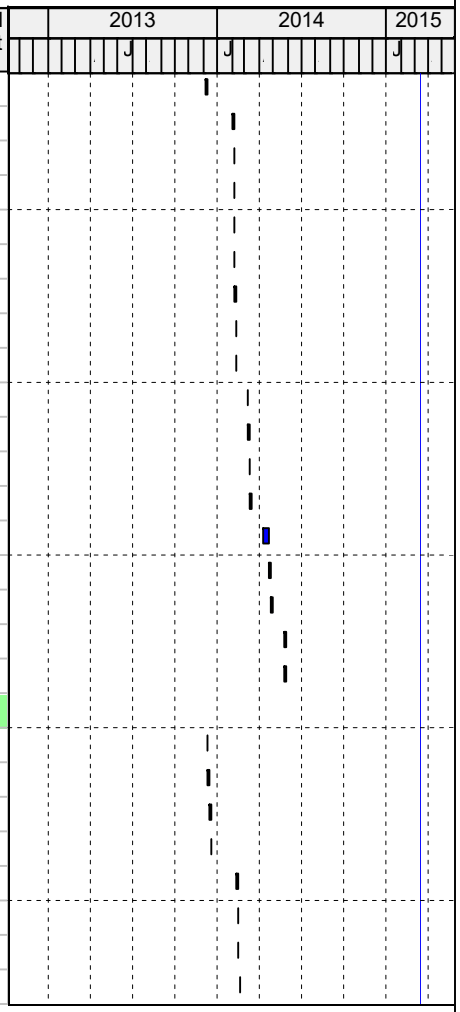



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 2 | 0 | 19-Feb-14 A | 20-Feb-14 A | |
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 2 | 0 | 21-Feb-14 A | 24-Feb-14 A | |
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 2 | 0 | 19-Mar-14 A | 20-Mar-14 A | |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 2 | 0 | 21-Mar-14 A | 22-Mar-14 A | |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 2 | 0 | 14-May-14 A | 15-May-14 A | |
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 2 | 0 | 16-May-14 A | 19-May-14 A | |
| S2-4038 | Stair 2 - Set Mtl Stairs / Railings L17 | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - Set Metal Stairs / Railings LL2 | 6 | 0 | 05-Mar-14 A | 20-Mar-14 A | |
| S3-4002 | Stair 3 - Set Metal Stairs / Railings LL1 | 6 | 0 | 17-Mar-14 A | 21-Mar-14 A | |
| S3-4004 | Stair 3 - Permanent Railings / Final Finishes | 4 | 4 | 31-Mar-15 | 03-Apr-15 | 26 |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |
| S4-4000 | Stair 4 - Set Metal Stairs / Railings LL2 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4002 | Stair 4 - Set Metal Stairs / Railings LL1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4004 | Stair 4 -Set Metal Stairs / Railings L1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4006 | Stair 4 - Permanent Railings / Final Finishes | 4 | 4 | 13-Apr-15 | 16-Apr-15 | 15 |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |
| S6-4000 | Stair 6 - Set Metal Stairs / Railings | 5 | 0 | 25-Jun-14 A | 01-Jul-14 A | |
| S6-4002 | Stair 6 - Permanent Railings / Final Finishes | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 39 |
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |

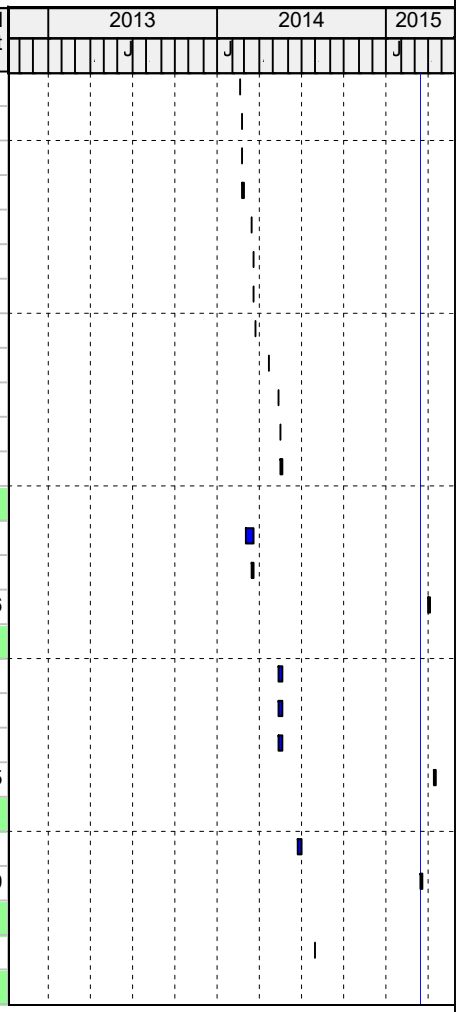



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes | 5 | 5 | 02-Apr-15 | 08-Apr-15 | 23 |
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a -Set Metal Stairs / Railings L1 | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| S4a-4002 | Stair 4a - Permanent Railings / Final Finishes | 2 | 2 | 17-Apr-15 | 20-Apr-15 | 15 |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 07-Jun-13 A | | |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 0 | 17-Jun-13 A | 21-Jun-13 A | |
| EL-1004 | Elev - Submittal Approval | 21 | 0 | 21-Jun-13 A | 01-Jan-14 A | |
| EL-1006 | Elev - Release to Manufacturing | 14 | 0 | 02-Jan-14 A | 15-Jan-14 A | |
| EL-1008 | Elev - Fabrication (Engineered Geared) | 95 | 0 | 16-Jan-14 A | 14-Jun-14 A | |
| EL-1010 | Elev - Machines delivered | 1 | 0 | 12-May-14 A | 12-May-14 A | |
| EL-1011 | Elev - Elevator Machines Flown & Set At Top Of Hoist | 5 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5016 | Elev 5 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-1216 | Elev 1&2 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-3416 | Elev 3&4 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-1202 | Elev 1&2 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-3402 | Elev 3&4 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-5018 | Elev 5 - Set Hoistway Machines | 3 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| EL-1218 | Elev 1&2 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-3418 | Elev 3&4 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-1200 | Elev 1&2 - Hoistway Clear & Ready (GC) | 0 | 0 | 20-Jun-14 A | | |
| EL-1204 | Elev 1&2 - Install Rails & Brackets | 17 | 0 | 23-Jun-14 A | 15-Jul-14 A | |
| EL-3400 | Elev 3&4 - Hoistway Clear & Ready (GC) | 0 | 0 | 23-Jun-14 A | | |
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 24-Jun-14 A | | |

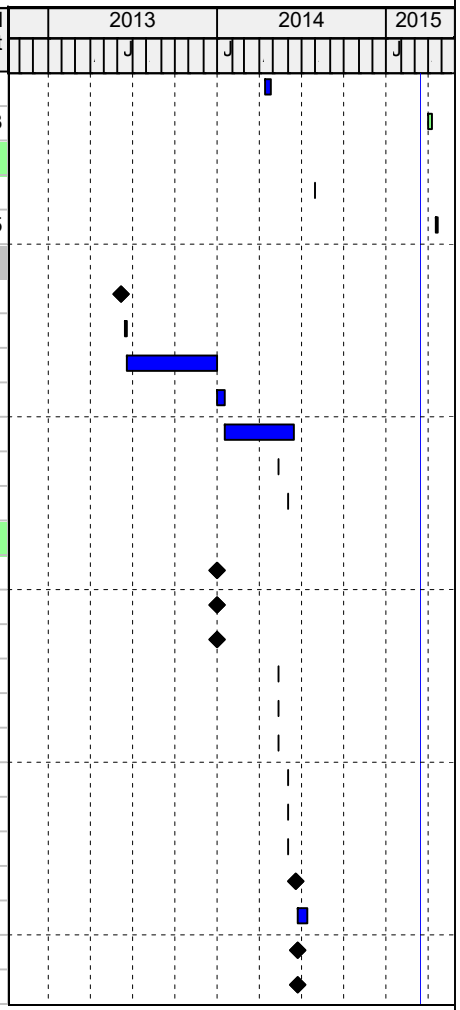



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-1206 | Elev 1&2 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Jul-14 A | |
| EL-1207 | Elev 1&2 - Install Pit Equipment/Car Sling/CWT Fram | 3 | 0 | 15-Jul-14 A | 01-Aug-14 A | |
| EL-1208 | Elev 1&2 - Install MHoist & Cable | 5 | 0 | 16-Jul-14 A | 24-Jul-14 A | |
| EL-3407 | Elev 3&4 - Install Pit Equipment/Car Sling/CWT Fram | 5 | 0 | 16-Jul-14 A | 06-Aug-14 A | |
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 21-Jul-14 A | | |
| EL-5004 | Elev 5 - Install Rails & Brackets | 13 | 0 | 21-Jul-14 A | 11-Aug-14 A | |
| EL-3404 | Elev 3&4 - Install Rails & Brackets | 18 | 0 | 23-Jul-14 A | 04-Aug-14 A | |
| EL-3406 | Elev 3&4 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 28-Jul-14 A | |
| EL-3408 | Elev 3&4 - Install Hoist & Cable | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| EL-5007 | Elev 5 - Install Pit Equipment/Car Sling/CWT Frame/V | 5 | 0 | 12-Aug-14 A | 15-Aug-14 A | |
| EL-1210 | Elev 1&2 - Install Entrances/Doors/Fixtures/Fascia | 19 | 0 | 14-Aug-14 A | 22-Sep-14 A | |
| EL-3410 | Elev 3&4 - Install Entrances/Doors/Fixtures/Fascia | 30 | 0 | 14-Aug-14 A | 02-Oct-14 A | |
| EL-5006 | Elev 5 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Aug-14 A | |
| EL-5008 | Elev 5 - Install MHoist & Cable | 4 | 0 | 18-Aug-14 A | 20-Aug-14 A | |
| EL-5010 | Elev 5 - Install Entrances/Doors/Fixtures/Fascia | 21 | 0 | 21-Aug-14 A | 26-Sep-14 A | |
| EL-1212 | Elev 1&2 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 22-Sep-14 A | 13-Oct-14 A | |
| EL-5012 | Elev 5 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 26-Sep-14 A | 16-Oct-14 A | |
| EL-3412 | Elev 3&4 - Install Hoistway Equipment/Pipe & Wire | 23 | 0 | 03-Oct-14 A | 03-Nov-14 A | |
| EL-1214 | Elev 1&2 - Install Cab/Wiring/Door Operator(s) | 11 | 0 | 14-Oct-14 A | 28-Oct-14 A | |
| EL-5014 | Elev 5 - Install Cab/Wiring/Door Operator(s) | 7 | 0 | 17-Oct-14 A | 27-Oct-14 A | |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 1 | 0 | 24-Oct-14 A | 24-Oct-14 A | |
| EL-6016 | Elev 6 - Hoistway Walls Complete (GC) | 0 | 0 | | 24-Oct-14 A | |
| EL-6004 | Elev 6 - Install Cylinders/Rails & Brackets | 4 | 0 | 27-Oct-14 A | 30-Oct-14 A | |
| EL-5022 | Elev 5 - Adjust | 5 | 0 | 28-Oct-14 A | 03-Nov-14 A | |
| EL-1222 | Elev 1&2 - Adjust | 5 | 0 | 29-Oct-14 A | 04-Nov-14 A | |
| EL-6006 | Elev 6 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 30-Oct-14 A | |
| EL-6007 | Elev 6 - Install Pit Equipment/Car Sling | 2 | 0 | 31-Oct-14 A | 03-Nov-14 A | |

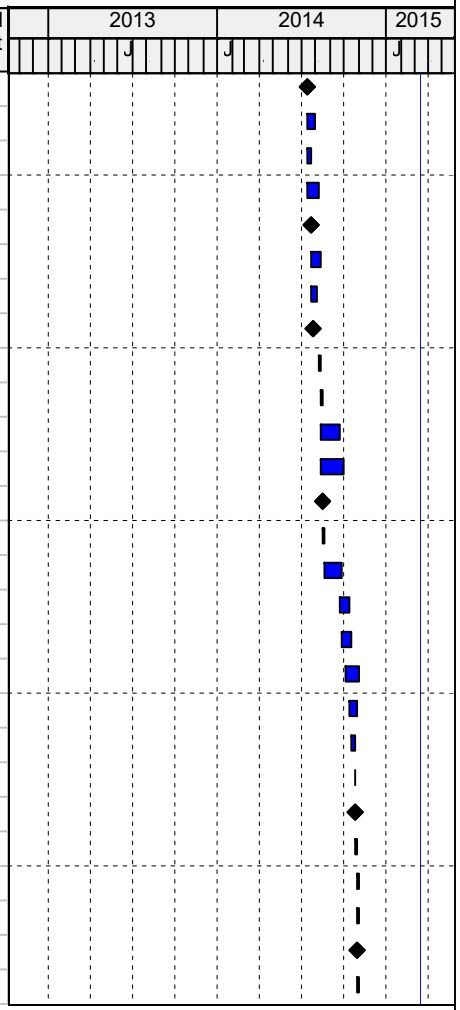


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| EL-3414 | Elev 3&4 - Install Cab/Wiring/Door Operator(s) | 10 | 0 | 04-Nov-14 A | 17-Nov-14 A | |
| EL-6018 | Elev 6 - Install Machine Room Equipment | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| EL-1224 | Elev 1&2 - Clean / Paint / Punchlist | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| EL-5026 | Elev 5 - Inspections | 7 | 0 | 13-Nov-14 A | 14-Nov-14 A | |
| EL-3422 | Elev 3&4 - Adjust | 8 | 0 | 18-Nov-14 A | 20-Nov-14 A | |
| EL-6012 | Elev 6 - Install hoistway rails & divider beams | 2 | 0 | 20-Nov-14 A | 21-Nov-14 A | |
| EL-6010 | Elev 6 - Install elevator fronts/rears | 9 | 0 | 09-Dec-14 A | 24-Dec-14 A | |
| EL-6014 | Elev 6 - Cab build-out | 5 | 0 | 15-Dec-14 A | 30-Jan-15 A | |
| EL-6022 | Elev 6 - Final cleaning at EMR | 4 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| EL-1226 | Elev 1&2 - CoB/L&I Inspections (for FF&E use) | 3 | 0 | 04-Mar-15 A | 06-Mar-15 A | |
| EL-3424 | Elev 3&4 - Walsh/TKE pre-inspection | 6 | 6 | 27-Mar-15* | 06-Apr-15 | 23 |
| EL-6024 | Elev 6 - Walsh/TKE pre-inspection | 2 | 2 | 02-Apr-15 | 06-Apr-15 | 25 |
| EL-3426 | Elev 3&4 - CoB/L&I Inspections (Final) | 3 | 3 | 08-Apr-15 | 10-Apr-15 | 21 |
| EL-6026 | Elev 6 - CoB/L&I Inspections (Final) | 1 | 1 | 10-Apr-15 | 10-Apr-15 | 21 |
| **Exterior Shell** | | | | | | |
| **Elevations** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2** | | | | | | |
| L3D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Feb-14 A | 12-Feb-14 A | |
| L3-5308 | L3- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 17-Feb-14 A | 21-Feb-14 A | |
| L4D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Feb-14 A | 19-Feb-14 A | |
| L4-5308 | L4- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Feb-14 A | 28-Feb-14 A | |
| L5D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Feb-14 A | 26-Feb-14 A | |
| L5-5308 | L5- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 03-Mar-14 A | 07-Mar-14 A | |
| L6D5308 | Deliver/Stock Wall Panels | 1 | 0 | 05-Mar-14 A | 05-Mar-14 A | |
| L6-5308 | L6- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |

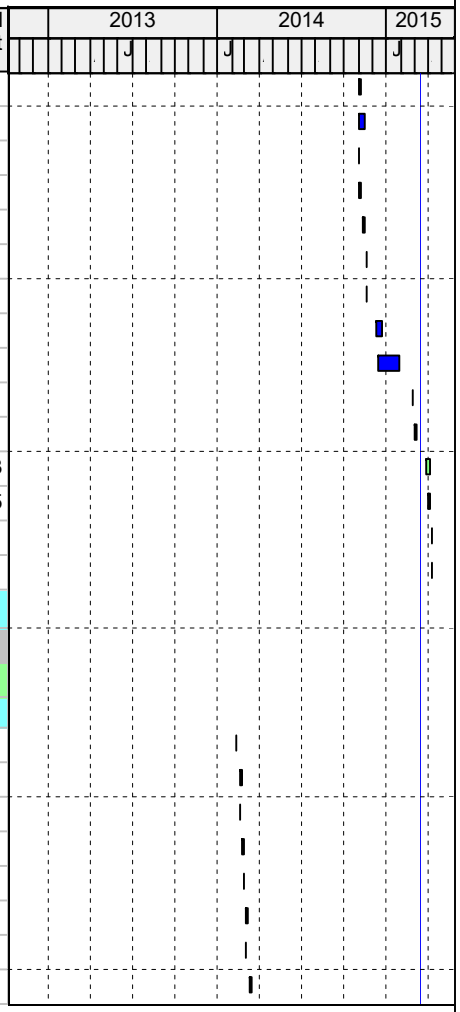



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L7-5308 | L7- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L7D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Mar-14 A | 12-Mar-14 A | |
| L8D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Mar-14 A | 19-Mar-14 A | |
| L8-5308 | L8- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Mar-14 A | 28-Mar-14 A | |
| L9D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L9-5308 | L9- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 31-Mar-14 A | 07-Apr-14 A | |
| 10D5308 | Deliver/Stock Wall Panels | 1 | 0 | 02-Apr-14 A | 02-Apr-14 A | |
| L10-5308 | L10- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 07-Apr-14 A | 11-Apr-14 A | |
| 11D5308 | Deliver/Stock Wall Panels | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L11-5308 | L11- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 11-Apr-14 A | 18-Apr-14 A | |
| 12D5308 | Deliver/Stock Wall Panels | 1 | 0 | 16-Apr-14 A | 16-Apr-14 A | |
| L12-5308 | L12- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Apr-14 A | 25-Apr-14 A | |
| 14D5308 | Deliver/Stock Wall Panels | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L14-5308 | L14 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Apr-14 A | 01-May-14 A | |
| 15D5308 | Deliver/Stock Wall Panels | 1 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L15-5308 | L15 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| 16D5308 | Deliver/Stock Wall Panels | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L16-5308 | L16- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| 17D5308 | Deliver/Stock Wall Panels | 1 | 0 | 14-May-14 A | 14-May-14 A | |
| L17-5308 | L17 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 20-May-14 A | 11-Jun-14 A | |
| LL2-5308 | LL2 Thru L4 - Support Frame/Sheathing for Metal Wa | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL1-5308 | LL1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| L1-5308 | L1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| **Level 1** | | | | | | |
| L3-5102 | L3- Storefront Frames | 7 | 0 | 18-Aug-14 A | 29-Sep-14 A | |
| L1-5102 | L1 - Storefront Frames (excl. Main Entry Facade) | 8 | 0 | 02-Sep-14 A | 11-Sep-14 A | |
| L1-5104 | L1 - Storefront Glazing (excl. Main Entry Facade) | 4 | 0 | 19-Sep-14 A | 24-Sep-14 A | |

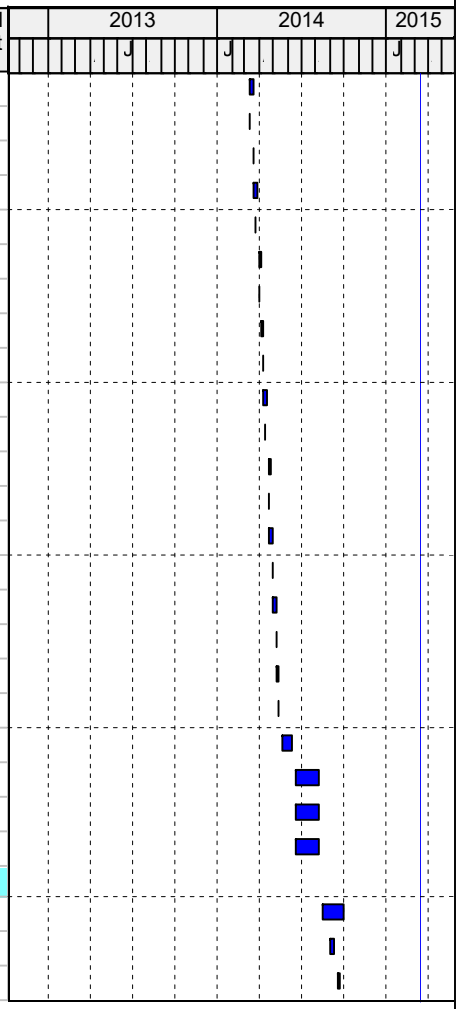



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EP-5110 | L1 - Revolving Doors | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L3-5104 | L3 - Storefront Glazing | 3 | 0 | 30-Sep-14 A | 03-Oct-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Levels 3-4** | | | | | | |
| L3-5130 | L3 - Install Punch Windows | 5 | 0 | 24-Feb-14 A | 10-Mar-14 A | |
| L4-5130 | L4 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 12-Mar-14 A | |
| L5-5130 | L5 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L6-5130 | L6- Install Punch Windows | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L7-5130 | L7 - Install Punch Windows | 5 | 0 | 18-Mar-14 A | 21-Mar-14 A | |
| L8-5130 | L8 - Install Punch Windows | 5 | 0 | 24-Mar-14 A | 28-Mar-14 A | |
| L9-5130 | L9 - Install Punch Windows | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L10-5130 | L10 - Install Punch Windows | 5 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-5130 | L11 - Install Punch Windows | 5 | 0 | 14-Apr-14 A | 21-Apr-14 A | |
| L12-5130 | L12 - Install Punch Windows | 5 | 0 | 22-Apr-14 A | 25-Apr-14 A | |
| L14-5130 | L14 - Install Punch Windows | 5 | 0 | 28-Apr-14 A | 05-May-14 A | |
| L15-5130 | L15 - Install Punch Windows | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| L16-5130 | L16 - Install Punch Windows | 5 | 0 | 12-May-14 A | 20-May-14 A | |
| L17-5130 | L17 - Install Punch Windows | 5 | 0 | 27-May-14 A | 16-Jun-14 A | |
| **Roofs** | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| RF-4026 | L1 - City Park - Protection Board | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| **Pool Membrane - (elev 18')** | | | | | | |
| RF-4034 | Pool - Install plumbing | 3 | 0 | 20-Oct-14 A | 22-Oct-14 A | |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |
| RF-4010 | AR - Set Mechanical Equipment | 5 | 0 | 10-Jun-14 A | 12-Jun-14 A | |

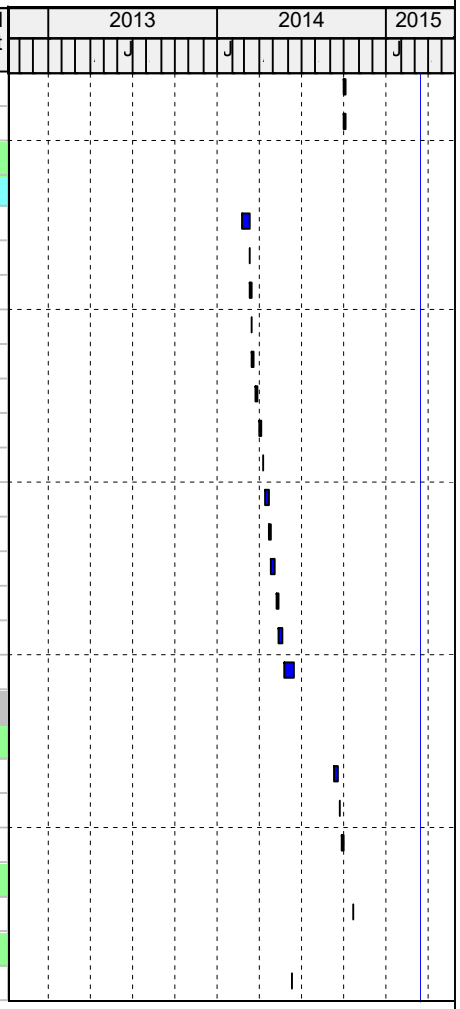



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 10 | 0 | 04-Aug-14 A | 27-Aug-14 A | |
| RF-4012 | L2.5 Horseshoe - Install corrugated metal panels | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 8 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |
| PC-4008 | RF - Entry / Porte Cochere Roofing System | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | RF - Upper Ballroom Roofing System | 3 | 0 | 28-Jul-14 A | 31-Jul-14 A | |
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 4 | 0 | 31-Jul-14 A | 04-Aug-14 A | |
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |
| RF-4018 | TR - Terrace Roof - Green Roofing System | 5 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| RF-4020 | TR - Terrace Roof - Install sheet metal capping[DELE | 1 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4022 | TR - Terrace Roof - Install deocrative metal railing | 3 | 3 | 17-Mar-15 | 19-Mar-15 | 29 |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Perimeter Framing / Sul | 10 | 0 | 02-Jun-14 A | 08-Jul-14 A | |
| RF-4002 | Tower Roof - Roofing System | 10 | 0 | 20-Aug-14 A | 17-Sep-14 A | |
| **PH - Roof - (elev 173')** | | | | | | |
| RF-4030 | PH - Roofing System | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| RF-4032 | PH - Coping / Flashing [DELETED] | 3 | 0 | 01-Sep-14 A | 01-Sep-14 A | |
| **Rough-In's** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6002 | LL4 - Layout | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| LL4-6008 | LL4 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL4-6012 | LL4 - Fire Sprinkler Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6014 | LL4 - Plumbing Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |

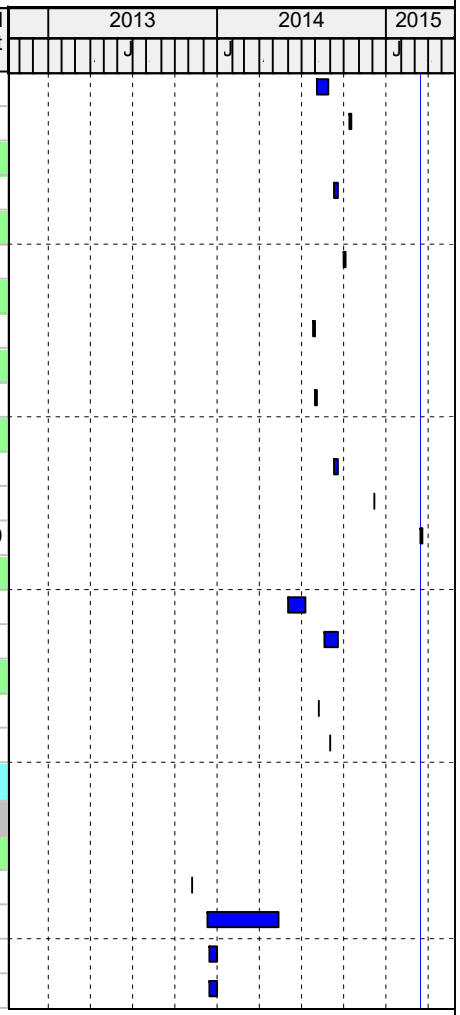


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-6018 | LL4 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6004 | LL4 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL4-6016 | LL4 - Electrical RI | 10 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties RI | 8 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6010 | LL4 - Elevator pits | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| LL4-6020 | LL4 - H Mtl Frames | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL4-6024 | LL4 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6002 | LL3 - Layout | 1 | 0 | 19-Nov-13 A | 19-Nov-13 A | |
| LL3-6008 | LL3 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL3-6012 | LL3 - Fire Sprinkler RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6014 | LL3 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6018 | LL3 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6004 | LL3 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL3-6020 | LL3 - H Mtl Frames | 3 | 0 | 08-May-14 A | 09-May-14 A | |
| LL3-6010 | LL3 - F/P Curbs | 5 | 0 | 19-May-14 A | 19-May-14 A | |
| LL3-6016 | LL3 - Electrical RI | 2 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties RI | 8 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL3-6024 | LL3 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6002 | LL2 - Layout | 1 | 0 | 14-Jan-14 A | 14-Jan-14 A | |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| LL2-6012 | LL2 - Fire Sprinkler RI | 10 | 0 | 21-Jan-14 A | 03-Feb-14 A | |
| LL2-6014 | LL2 - Plumbing RI | 10 | 0 | 21-Jan-14 A | 14-Feb-14 A | |
| LL2E-6016 | LL2 - Electrical RI | 8 | 0 | 03-Feb-14 A | 17-Mar-14 A | |

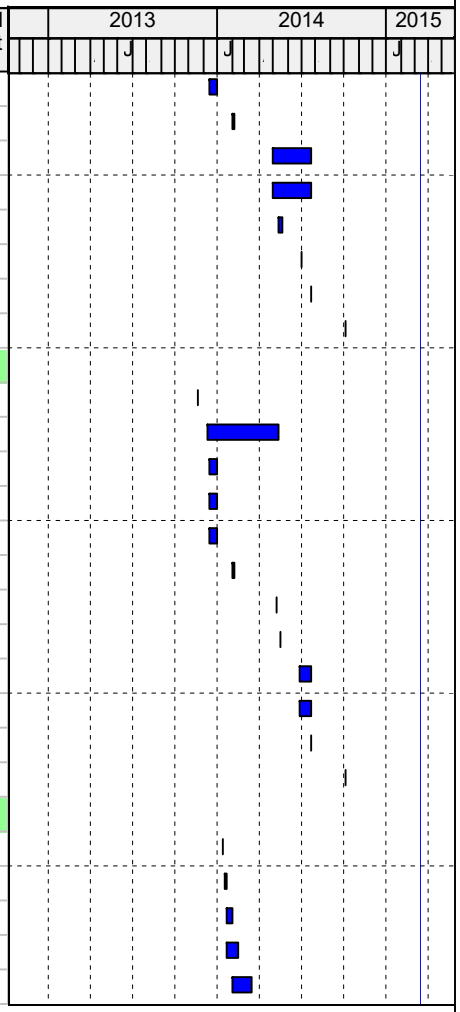



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-6016 | LL2 - Electrical RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2-6018 | LL2 - HVAC RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2–6004 | LL2 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL2E-6004 | LL2 - CMU Walls | 10 | 0 | 04-Mar-14 A | 09-May-14 A | |
| LL2E-6012 | LL2 - Fire Sprinkler RI | 8 | 0 | 21-Mar-14 A | 01-Apr-14 A | |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 24-Apr-14 A | |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 3 | 0 | 23-Apr-14 A | 21-Jul-14 A | |
| LL2E-6020 | LL2 - H Mtl Frames | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| LL2-6020 | LL2 - H Mtl Frames | 3 | 0 | 12-May-14 A | 13-May-14 A | |
| LL2E-6008 | LL2 - Int Wall Framing | 5 | 0 | 13-May-14 A | 22-Jun-14 A | |
| LL2E-6014 | LL2 - Plumbing RI | 8 | 0 | 13-May-14 A | 30-May-14 A | |
| LL2E-6018 | LL2 - HVAC RI | 8 | 0 | 13-May-14 A | 04-Aug-14 A | |
| LL2E-6022 | LL2 - Fire Alarm / Elec Specialties RI (East of 10) | 8 | 0 | 13-May-14 A | 22-Sep-14 A | |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties RI (West of 10) | 8 | 0 | 19-May-14 A | 22-Sep-14 A | |
| LL2-6015 | LL2 - Main Elect Room Set Equip / RI - Power to Ma | 15 | 0 | 30-Jun-14 A | 26-Sep-14 A | |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 0 | 16-Jul-14 A | 21-Jul-14 A | |
| LL2-6024 | LL2 - Inspections | 2 | 0 | 15-Sep-14 A | 03-Oct-14 A | |
| LL2-6010 | F/P Curbs at Garage | 5 | 5 | 30-Mar-15 | 03-Apr-15 | 26 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6002 | Layout | 3 | 0 | 03-Jan-14 A | 08-Jan-14 A | |
| LL1-6008 | Int Wall Framing & Inspection | 6 | 0 | 08-Jan-14 A | 21-Jul-14 A | |
| LL1-Z2-6002 | Layout | 3 | 0 | 08-Jan-14 A | 14-Jan-14 A | |
| LL1-Z3-6002 | Layout | 3 | 0 | 14-Jan-14 A | 17-Jan-14 A | |
| LL1-Z2-6008 | Int Wall Framing & Inspection | 6 | 0 | 17-Jan-14 A | 01-Aug-14 A | |
| LL1-Z3-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-Jan-14 A | 04-Aug-14 A | |
| LL1-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 09-May-14 A | |

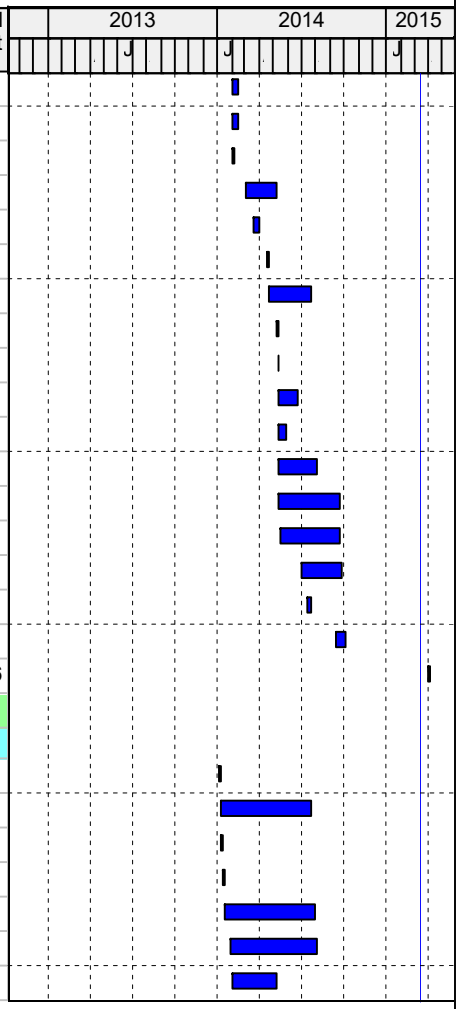


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 28-Apr-14 A | |
| LL1-Z3-6004 | CMU Walls (At All Areas North of Q-Line) | 3 | 0 | 03-Feb-14 A | 13-May-14 A | |
| LL1C-6012 | Complete Fire Sprinkler RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6016 | Complete Electrical RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 10 | 0 | 17-Feb-14 A | 16-Sep-14 A | |
| LL1C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 30-Apr-14 A | |
| LL1-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-Z2-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z2-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z3-6012 | Fire Sprinkler RI (At All Areas North of Q-Line) | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z3-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 11-Sep-14 A | |
| LL1-Z3-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z2C-6012 | Complete Fire Sprinkler RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6014 | Complete Plumbing RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6016 | Complete Electrical RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 15 | 0 | 24-Feb-14 A | 15-Sep-14 A | |
| LL1-Z2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2-6020 | Hollow Metal Door Frames | 5 | 0 | 17-Mar-14 A | 04-Apr-14 A | |

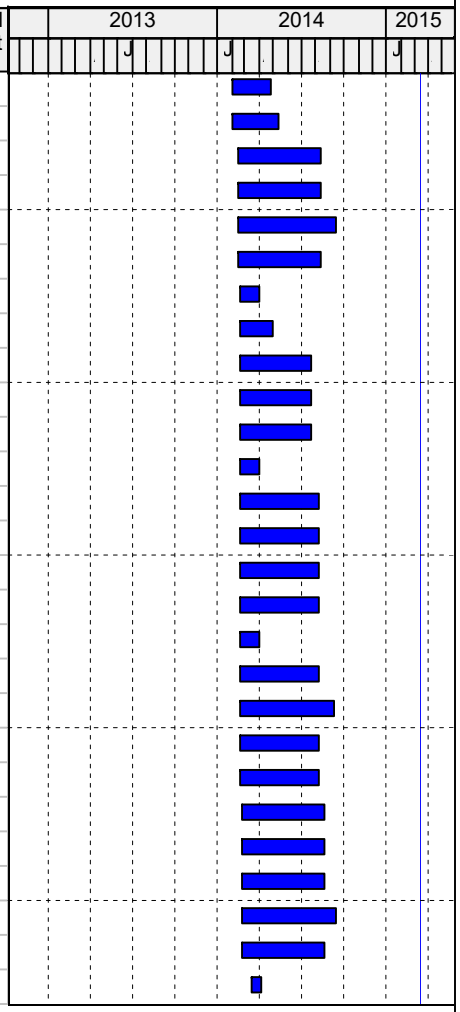



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| LL1-Z3-6020 | Hollow Metal Door Frames (At All Areas North of Q-Lir | 1 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| L1B-6004 | CMU Walls [including East Service Corridor] | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L1L-6002 | Layout [including back of house] | 3 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 29-Apr-14 A | |
| L1B-6008 | Int Wall Framing & Inspection | 6 | 0 | 21-Apr-14 A | 08-Aug-14 A | |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 5 | 0 | 25-Apr-14 A | 21-Jul-14 A | |
| LL1C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L1K-6004 | CMU Walls [including public restroom] | 3 | 0 | 05-May-14 A | 08-May-14 A | |
| L1K-6002 | Layout [including public restroom] | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| L1K-6008 | Int Wall Framing & Inspection | 4 | 0 | 09-May-14 A | 22-Aug-14 A | |
| L1B-6002 | Layout [including East Service Corridor] | 3 | 0 | 14-May-14 A | 27-May-14 A | |
| L1L-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-May-14 A | 06-Oct-14 A | |
| L1L-6004 | CMU Walls [including back of house] | 3 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L1K-6012 | Fire Sprinkler RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6014 | Plumbing RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6016 | Electrical RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1K-6018 | HVAC RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1B-6014 | Plumbing RI [including East Service Corridor] | 10 | 0 | 16-Jun-14 A | 24-Jun-14 A | |
| L1B-6018 | HVAC RI | 10 | 0 | 20-Jun-14 A | 15-Aug-14 A | |
| L1B-6012 | Fire Sprinkler RI | 10 | 0 | 21-Jun-14 A | 15-Aug-14 A | |
| L1L-6018 | HVAC RI | 5 | 0 | 23-Jun-14 A | 13-Oct-14 A | |
| L1L-6014 | Plumbing RI | 5 | 0 | 24-Jun-14 A | 28-Oct-14 A | |
| L1L-6010 | CMU Seismic Clips [including back of house] [DELET | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1L-6012 | Fire Sprinkler RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |
| L1L-6016 | Electrical RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |
| L1L-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 27-Jun-14 A | 13-Oct-14 A | |

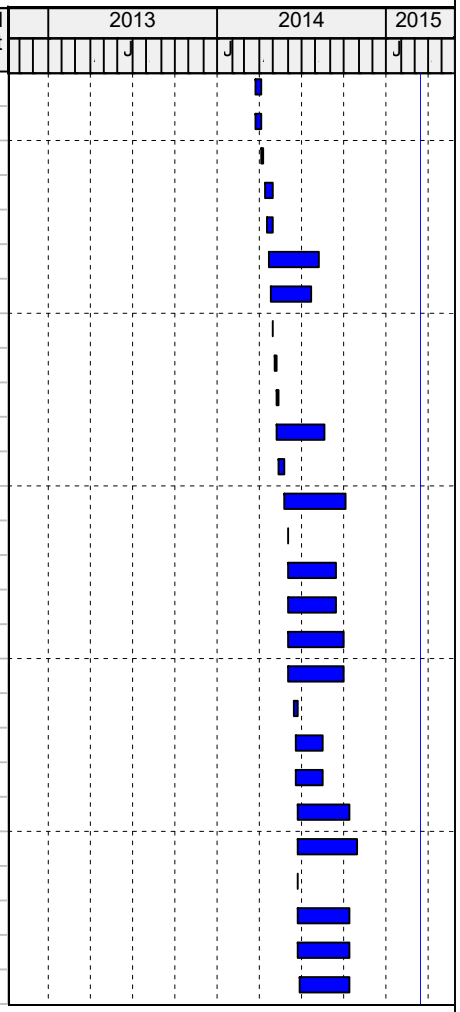



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 27-Jun-14 A | 29-Sep-14 A | |
| LL1-Z3-6009 | Frame Ceilings [DELETED] | 4 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1B-6016 | Electrical RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| L1B-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| LL1-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-Z2-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L1B-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-6024 | Inspections for Cover | 1 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L1B-6020 | Hollow Metal Door Frames | 5 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| LL1-Z3-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L1K-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 06-Aug-14 A | |
| LL1-Z2-6024 | Inspections for Cover | 2 | 0 | 07-Aug-14 A | 08-Aug-14 A | |
| L1K-6020 | Hollow Metal Door Frames | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-Z2-6009 | Frame Ceilings & Inspection | 6 | 0 | 22-Aug-14 A | 13-Oct-14 A | |
| L1L-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Aug-14 A | 13-Oct-14 A | |
| LL1-6009 | Frame Ceilings & Inspection (except for bar redesign | 9 | 0 | 02-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3-6024 | Inspections for Cover | 2 | 0 | 12-Sep-14 A | 12-Sep-14 A | |
| LL1-Z3C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6016 | Complete Electrical RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3C-6018 | Complete HVAC RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| L1KC-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 4 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L1B-6024 | Inspections for Cover (Main Ballroom N/S/W Walls & | 3 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1K-6024 | Inspections for Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1KC-6014 | Complete Plumbing RI @ Ceilings & Inspection | 4 | 0 | 02-Oct-14 A | 07-Oct-14 A | |
| L1BC-6014 | Complete Plumbing RI @ Ceilings | 7 | 0 | 06-Oct-14 A | 08-Oct-14 A | |

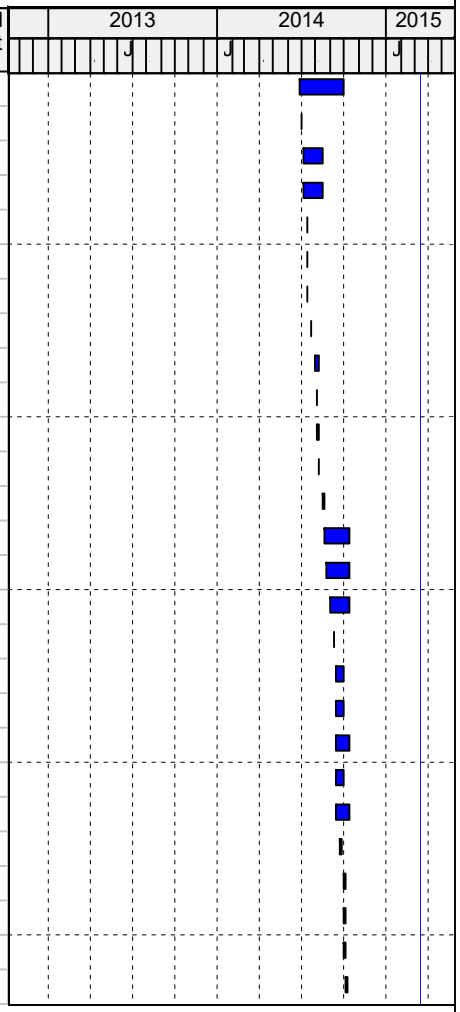


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1KC-6018 | Complete HVAC RI @ Ceilings & Inspection | 4 | 0 | 06-Oct-14 A | 10-Nov-14 A | |
| L1KC-6016 | Complete Electrical RI @ Ceilings & Inspection | 3 | 0 | 20-Oct-14 A | 10-Nov-14 A | |
| L1KC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 3 | 0 | 20-Oct-14 A | 10-Nov-14 A | |
| L1L-6024 | Inspections for Cover | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L1L-6009 | Frame ceilings & inspection at high ceiling | 13 | 0 | 24-Nov-14 A | 20-Jan-15 A | |
| L1B-6009 | Frame Ceilings & inspection at Main Ballroom (per re | 5 | 0 | 04-Dec-14 A | 16-Jan-15 A | |
| L1LC-6012 | Complete fire sprinkler RI @ ceilings | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1LC-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| L1LC-6016 | Complete electrical rough-in @ ceilings & inspection | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1LC-6018 | Complete HVAC RI @ Ceilings | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1LC-6022 | Complete fire alarm/elec specialties RI @ ceilings & ir | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1K-6009 | Frame ceilings & inspection at public restroom | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L1B-8112 | Fire sprinkler trim at Ballrooms | 2 | 2 | 31-Mar-15 | 01-Apr-15 | 5 |
| L1B-8118 | Lighting & electrical trim at Ballrooms | 5 | 5 | 31-Mar-15 | 06-Apr-15 | 0 |
| L1B-8204 | HVAC trim at Ballrooms | 5 | 5 | 31-Mar-15 | 06-Apr-15 | 0 |
| L1BC-6022 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 31-Mar-15 | 01-Apr-15 | 5 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 0 | 17-Apr-14 A | 09-May-14 A | |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6006 | L2 - Support Frame/Sheathing for Metal Panels | 6 | 0 | 23-Apr-14 A | 07-Aug-14 A | |
| L02-6008 | L2 - Int Wall Framing | 10 | 0 | 25-Apr-14 A | 17-Jul-14 A | |
| L02-6014 | L2 - Plumbing RI | 15 | 0 | 28-Apr-14 A | 07-Aug-14 A | |
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 0 | 28-Apr-14 A | 09-May-14 A | |
| L02-6004 | L2 - CMU Walls | 5 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L02-6002 | L2 - Layout | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L02-6018 | L2 - HVAC RI (including equipment) | 20 | 0 | 18-Jun-14 A | 10-Sep-14 A | |

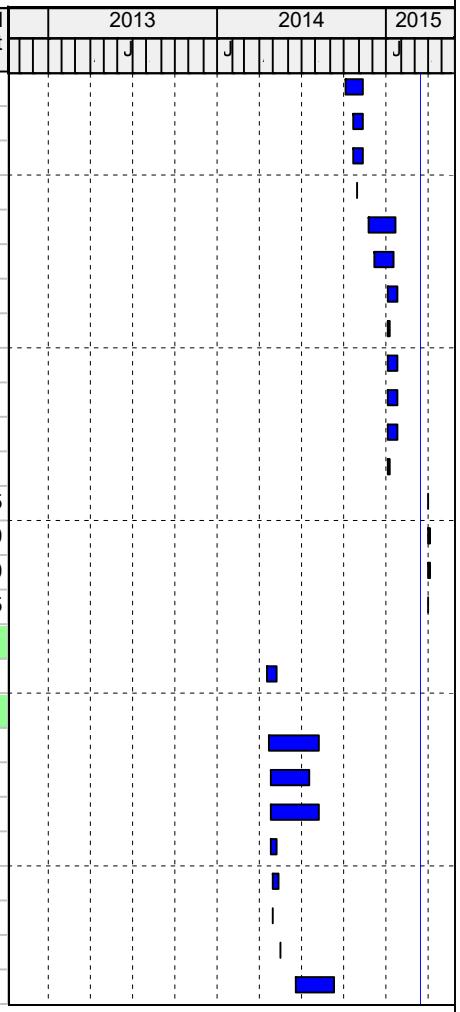


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-6016 | L2 - Electrical RI | 10 | 0 | 24-Jun-14 A | 14-Aug-14 A | |
| L02-6022 | L2 - Fire Alarm / Elec Specialties RI | 10 | 0 | 24-Jun-14 A | 10-Oct-14 A | |
| L02-6012 | L2 - Fire Sprinkler RI | 10 | 0 | 26-Jun-14 A | 07-Aug-14 A | |
| L02-6020 | L2 - H Mtl Frames | 5 | 0 | 11-Jul-14 A | 17-Jul-14 A | |
| L02-6024 | L2 - Inspections - North Half | 2 | 0 | 10-Oct-14 A | 20-Oct-14 A | |
| Upper Tower - (Levels 3 thru PH) | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L07-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 01-Apr-11 A | 11-Apr-11 A | |
| L04-6012 | Fire Sprinkler Mains | 5 | 0 | 01-Feb-14 A | 03-Apr-14 A | |
| L03-8219 | HVAC Risers | 5 | 0 | 11-Feb-14 A | 23-Mar-14 A | |
| L03-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 11-Feb-14 A | 03-Mar-14 A | |
| L03-6002 | Layout | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| L04-8219 | HVAC Risers | 5 | 0 | 13-Feb-14 A | 23-Mar-14 A | |
| L05-8219 | HVAC Risers | 5 | 0 | 17-Feb-14 A | 03-Mar-14 A | |
| L03-6008 | Frame Shaft Walls | 3 | 0 | 18-Feb-14 A | 26-Mar-14 A | |
| L04-6002 | Layout | 5 | 0 | 19-Feb-14 A | 25-Feb-14 A | |
| L04-6008 | Frame Shaft Walls | 3 | 0 | 20-Feb-14 A | 26-Mar-14 A | |
| L03-6011 | PreRock Shafts | 2 | 0 | 24-Feb-14 A | 25-Mar-14 A | |
| L03-6010 | Frame Walls | 5 | 0 | 25-Feb-14 A | 25-Mar-14 A | |
| L05-6002 | Layout | 5 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| L04-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 28-Feb-14 A | 05-Mar-14 A | |
| L03-6016 | Electrical RI | 5 | 0 | 03-Mar-14 A | 04-Apr-14 A | |
| L03-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 12-Mar-14 A | |
| L04-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 13-Mar-14 A | |
| L04-6010 | Frame Walls | 5 | 0 | 04-Mar-14 A | 05-Jun-14 A | |
| L05-6008 | Frame Shaft Walls | 3 | 0 | 05-Mar-14 A | 27-Mar-14 A | |
| L06-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |

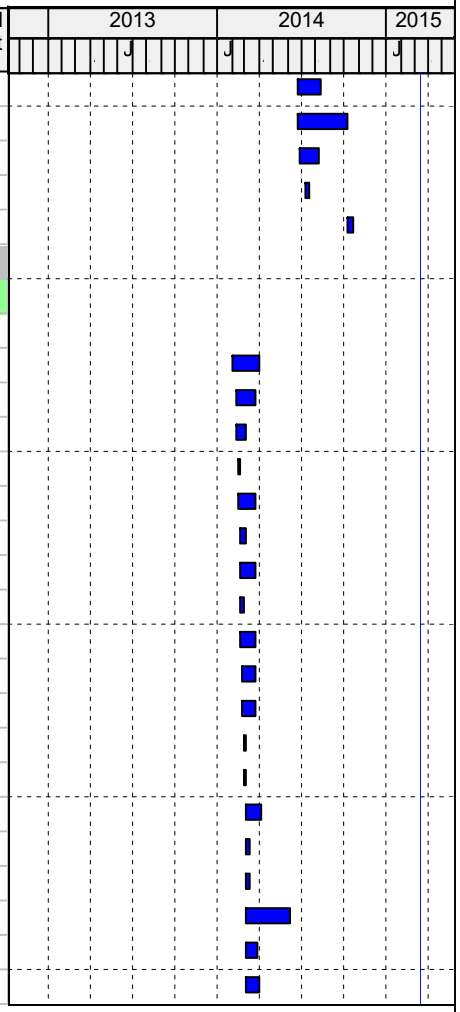



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L05-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 06-Mar-14 A | 21-Mar-14 A | |
| L03-6020 | Install Hollow Metal Frames | 3 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L04-6020 | Install Hollow Metal Frames | 3 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L05-6010 | Frame Walls | 5 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L06-6002 | Layout | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L04-6011 | PreRock Shafts | 2 | 0 | 18-Mar-14 A | 25-Mar-14 A | |
| L05-6009 | Inspect Shafts | 1 | 0 | 18-Mar-14 A | 18-Mar-14 A | |
| L05-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| L06-6008 | Frame Shaft Walls | 3 | 0 | 19-Mar-14 A | 03-Apr-14 A | |
| L06-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 27-Mar-14 A | |
| L04-6016 | Electrical RI | 5 | 0 | 20-Mar-14 A | 09-Apr-14 A | |
| L05-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 26-Mar-14 A | |
| L06-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 07-Apr-14 A | |
| L07-6002 | Layout | 5 | 0 | 24-Mar-14 A | 30-Apr-14 A | |
| L03-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L03-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L05-6016 | Electrical RI | 5 | 0 | 25-Mar-14 A | 05-Jun-14 A | |
| L04-6019 | Complete Top Out GWB | 2 | 0 | 26-Mar-14 A | 06-Jun-14 A | |
| L05-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L06-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| L03-6019 | Complete Top Out GWB | 2 | 0 | 27-Mar-14 A | 02-May-14 A | |
| L08-6002 | Layout | 5 | 0 | 27-Mar-14 A | 02-Apr-14 A | |
| L05-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 28-Mar-14 A | 03-Apr-14 A | |
| L06-6010 | Frame Walls | 5 | 0 | 28-Mar-14 A | 07-Apr-14 A | |

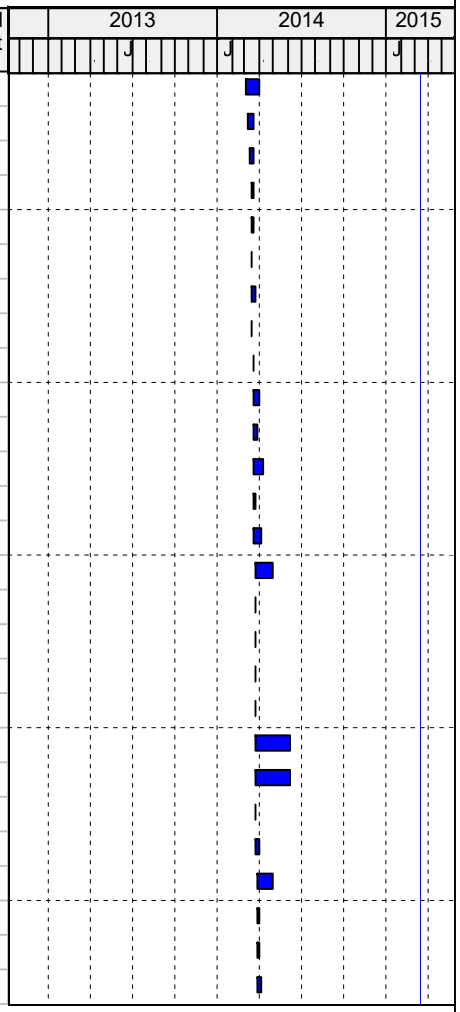



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6012 | Fire Sprinkler Mains | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L07-6008 | Frame Shaft Walls | 3 | 0 | 31-Mar-14 A | 03-Apr-14 A | |
| L05-6019 | Complete Top Out GWB | 2 | 0 | 01-Apr-14 A | 08-Apr-14 A | |
| L08-6008 | Frame Shaft Walls | 3 | 0 | 02-Apr-14 A | 21-Apr-14 A | |
| L03-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L04-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L05-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L06-6016 | Electrical RI | 5 | 0 | 03-Apr-14 A | 15-Apr-14 A | |
| L07-6009 | Inspect Shafts | 1 | 0 | 03-Apr-14 A | 03-Apr-14 A | |
| L07-6011 | PreRock Shafts | 2 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| L05-6012 | Fire Sprinkler Mains | 5 | 0 | 04-Apr-14 A | 30-Apr-14 A | |
| L06-6012 | Fire Sprinkler Mains | 5 | 0 | 07-Apr-14 A | 30-Apr-14 A | |
| L06-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L06-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L07-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| L07-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L03-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L03-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L04-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L06-6009 | Inspect Shafts | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L06-6019 | Complete Top Out GWB | 2 | 0 | 08-Apr-14 A | 18-Apr-14 A | |
| L07-6010 | Frame Walls | 5 | 0 | 08-Apr-14 A | 15-Apr-14 A | |
| L08-6011 | PreRock Shafts | 2 | 0 | 08-Apr-14 A | 23-Apr-14 A | |
| L09-6002 | Layout | 5 | 0 | 08-Apr-14 A | 26-Apr-14 A | |
| L03-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 09-Apr-14 A | 08-May-14 A | |
| L03-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L05-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 09-Apr-14 A | 14-Apr-14 A | |

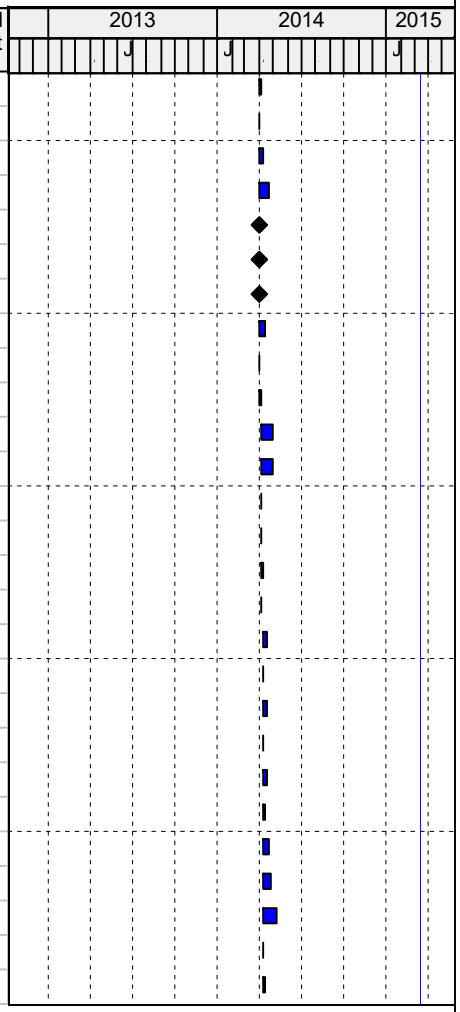



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-6009 | Inspect Shafts | 1 | 0 | 09-Apr-14 A | 25-Apr-14 A | |
| L09-6008 | Frame Shaft Walls | 3 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| L08-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| L04-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 15-Apr-14 A | 16-Apr-14 A | |
| L07-6012 | Fire Sprinkler Mains | 5 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| L07-6016 | Electrical RI | 5 | 0 | 15-Apr-14 A | 12-May-14 A | |
| L07-6020 | Install Hollow Metal Frames | 3 | 0 | 16-Apr-14 A | 23-Apr-14 A | |
| L05-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 17-Apr-14 A | 25-Apr-14 A | |
| L06-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 17-Apr-14 A | 12-May-14 A | |
| L06-6023 | Inspection of Exterior Framing | 0 | 0 | 17-Apr-14 A | | |
| L09-8219 | HVAC Risers | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L09-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L04-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 18-Apr-14 A | 20-Apr-14 A | |
| L04-6028 | PreRock at Heat Pumps | 2 | 0 | 20-Apr-14 A | 22-Apr-14 A | |
| L08-8219 | HVAC Risers | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6009 | Inspect Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6011 | PreRock Shafts | 2 | 0 | 22-Apr-14 A | 24-Apr-14 A | |
| L04-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L06-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 23-Apr-14 A | 25-Apr-14 A | |
| L08-6020 | Install Hollow Metal Frames | 3 | 0 | 23-Apr-14 A | 13-May-14 A | |
| L11-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L11-8220 | Plumbing Risers - Install | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L04-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L09-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L10-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |

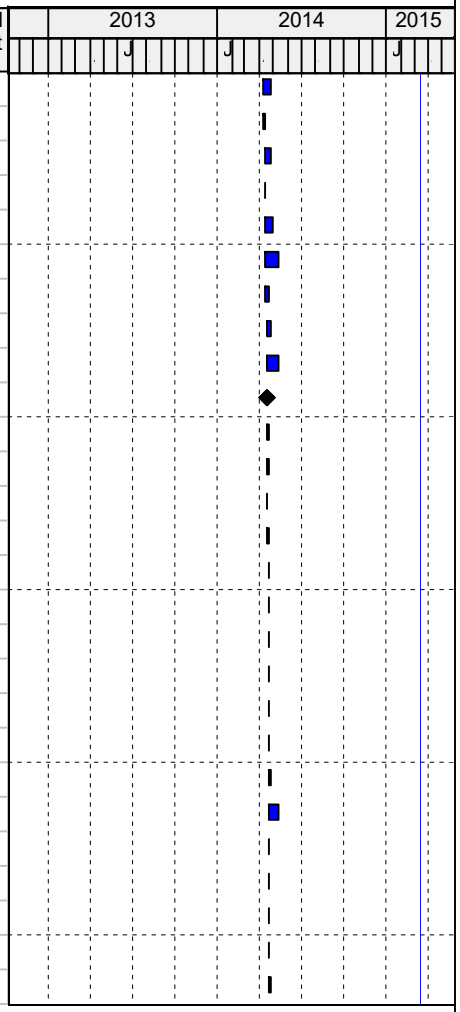



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 20-May-14 A | |
| L12-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L04-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 25-Apr-14 A | 11-Jun-14 A | |
| L04-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L09-6010 | Frame Walls | 5 | 0 | 25-Apr-14 A | 20-May-14 A | |
| L09-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L10-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L11-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 30-Apr-14 A | |
| L12-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L08-6010 | Frame Walls | 5 | 0 | 26-Apr-14 A | 30-Apr-14 A | |
| L10-6002 | Layout | 5 | 0 | 27-Apr-14 A | 27-Apr-14 A | |
| L04-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 28-Apr-14 A | 30-Apr-14 A | |
| L05-6018 | HVAC RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6028 | PreRock at Heat Pumps | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L07-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 28-Apr-14 A | 12-May-14 A | |
| L10-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-Apr-14 A | 22-May-14 A | |
| L11-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L12-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L05-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| L05-6028 | PreRock at Heat Pumps | 2 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L06-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 09-May-14 A | |

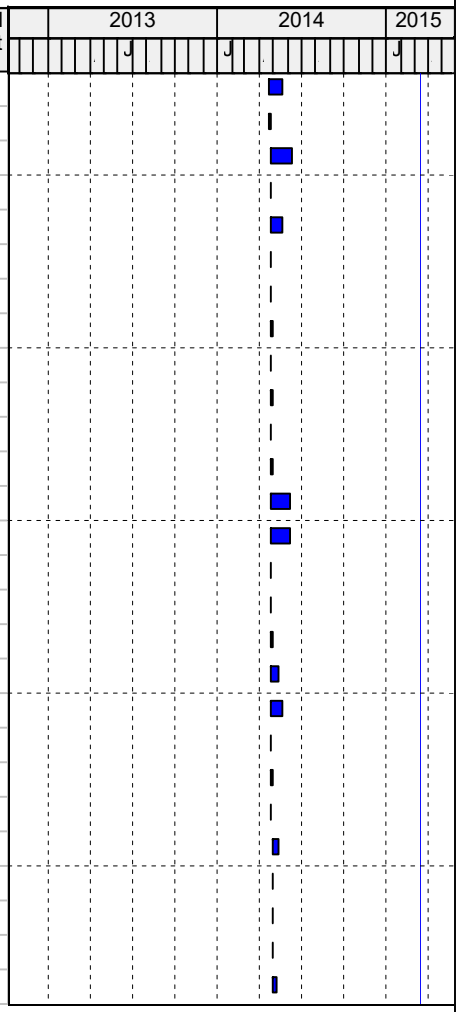



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L06-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L08-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L08-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L09-6020 | Install Hollow Metal Frames | 3 | 0 | 29-Apr-14 A | 20-May-14 A | |
| L09-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L10-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L04-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 30-Apr-14 A | 02-May-14 A | |
| L09-6019 | Complete Top Out GWB | 2 | 0 | 30-Apr-14 A | 06-Jun-14 A | |
| L11-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L12-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L03-6028 | PreRock at Heat Pumps | 2 | 0 | 01-May-14 A | 02-May-14 A | |
| L05-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L06-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L03-6014 | Set Tubs & Plumbing RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L05-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L05-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| L06-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L06-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 09-May-14 A | |
| L03-6018 | HVAC RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L03-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 06-May-14 A | 06-May-14 A | |
| L07-6014 | Set Tubs & Plumbing RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L07-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 06-May-14 A | 09-May-14 A | |

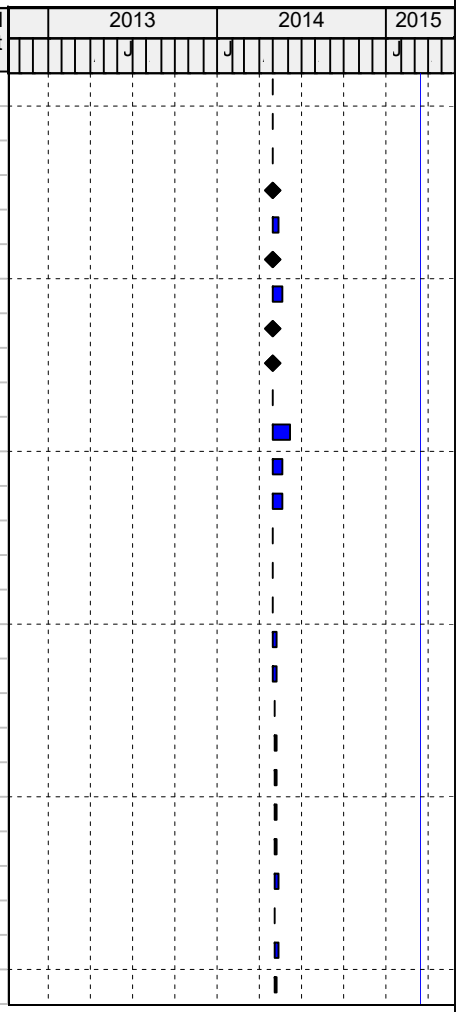



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6004 | CMU Wall/Clips | 3 | 0 | 07-May-14 A | 08-May-14 A | |
| L03-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L03-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 08-May-14 A | 13-May-14 A | |
| L03-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6004 | CMU Walls | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6018 | HVAC RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L11-6010 | Frame Walls | 5 | 0 | 09-May-14 A | 15-May-14 A | |
| L05-6014 | Set Tubs & Plumbing RI | 5 | 0 | 12-May-14 A | 05-Jun-14 A | |
| L07-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 12-May-14 A | 13-May-14 A | |
| L11-6020 | Install Hollow Metal Frames | 3 | 0 | 12-May-14 A | 14-May-14 A | |
| L11-6019 | Complete Top Out GWB | 2 | 0 | 12-May-14 A | 14-May-14 A | |
| L14-6002 | Layout | 5 | 0 | 12-May-14 A | 14-May-14 A | |
| L15-6002 | Layout | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L05-6004 | CMU Walls | 3 | 0 | 13-May-14 A | 13-May-14 A | |
| L06-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 25-Jun-14 A | |
| L06-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 13-May-14 A | 14-Jul-14 A | |
| L07-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 05-Jun-14 A | |
| L07-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| L07-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 13-May-14 A | 13-May-14 A | |
| L14-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L16-6002 | Layout | 5 | 0 | 13-May-14 A | 16-May-14 A | |
| L06-6004 | CMU Walls | 3 | 0 | 14-May-14 A | 14-May-14 A | |
| L07-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 15-May-14 A | |
| L08-6012 | Fire Sprinkler Mains | 5 | 0 | 15-May-14 A | 20-May-14 A | |

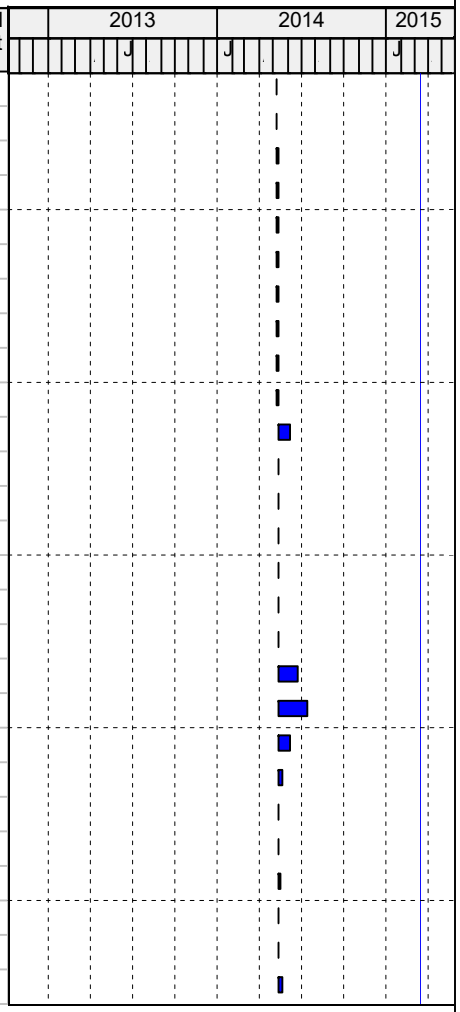



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6002 | Layout | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L07-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 16-May-14 A | 25-Jun-14 A | |
| L08-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L11-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L12-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L07-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L08-6028 | PreRock at Heat Pumps | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L09-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L10-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L11-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L15-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 19-May-14 A | 19-May-14 A | |
| L07-6028 | PreRock at Heat Pumps | 2 | 0 | 20-May-14 A | 21-May-14 A | |
| L07-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L08-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 20-May-14 A | 21-May-14 A | |
| L10-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L11-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L14-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L07-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 21-May-14 A | 27-May-14 A | |
| L08-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L08-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |

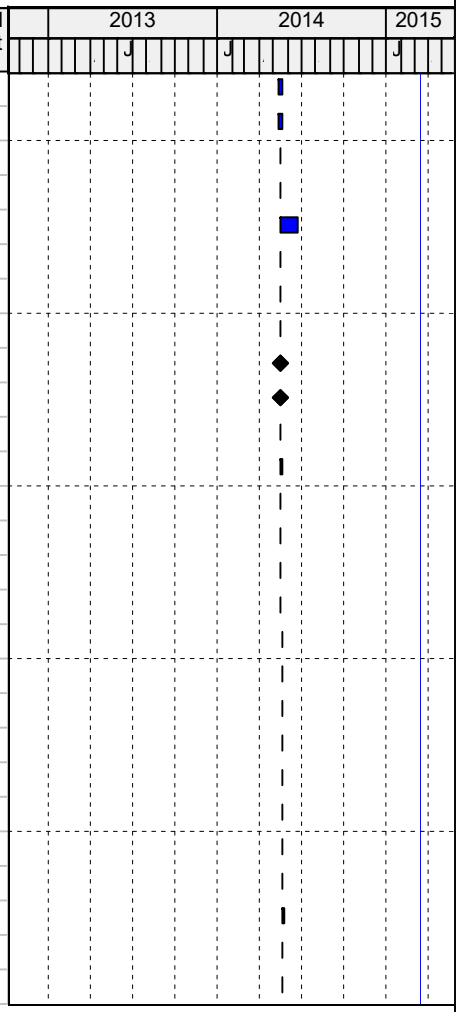


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6028 | PreRock at Heat Pumps | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L10-6014 | Set Tubs & Plumbing RI | 5 | 0 | 21-May-14 A | 27-Jun-14 A | |
| L10-6010 | Frame Walls | 5 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6019 | Complete Top Out GWB | 2 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L11-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L12-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L14-8220 | Plumbing Risers - Install | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L15-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L16-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L07-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| L08-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 22-May-14 A | 22-May-14 A | |
| L10-6012 | Fire Sprinkler Mains | 5 | 0 | 22-May-14 A | 27-May-14 A | |
| L08-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L09-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6020 | Install Hollow Metal Frames | 3 | 0 | 23-May-14 A | 03-Jun-14 A | |
| L10-6028 | PreRock at Heat Pumps | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L14-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L15-8220 | Plumbing Risers - Install | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L09-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 27-May-14 A | 27-May-14 A | |
| L12-6010 | Frame Walls | 5 | 0 | 27-May-14 A | 02-Jun-14 A | |
| L08-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L09-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 28-May-14 A | 28-May-14 A | |
| L10-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 28-May-14 A | 03-Jun-14 A | |
| L14-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L15-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-May-14 A | 30-May-14 A | |
| L16-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 28-May-14 A | 28-May-14 A | |

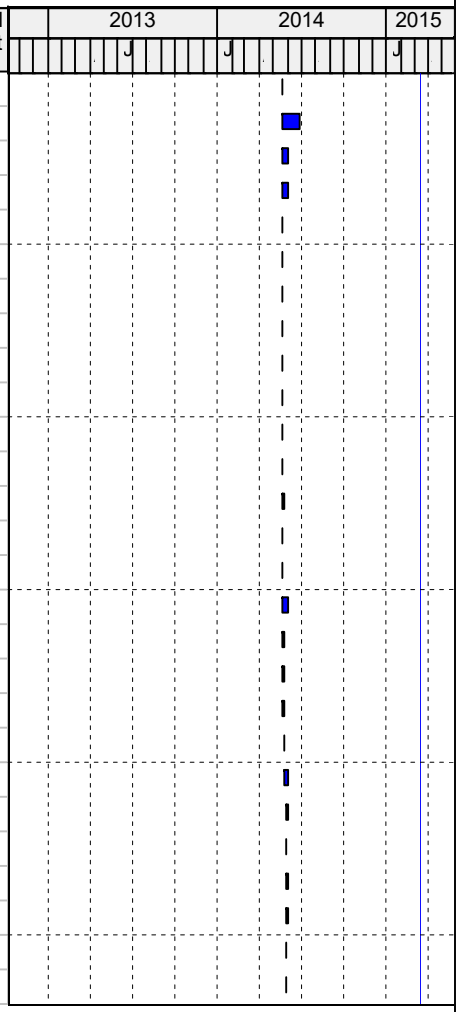


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8220 | Plumbing Risers - Install | 2 | 0 | 28-May-14 A | 29-May-14 A | |
| L08-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 29-May-14 A | 30-May-14 A | |
| L10-6016 | Electrical RI | 5 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L10-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| L12-6012 | Fire Sprinkler Mains | 5 | 0 | 30-May-14 A | 26-Jun-14 A | |
| L12-6020 | Install Hollow Metal Frames | 3 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L15-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L17-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L17-8220 | Plumbing Risers - Install | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L10-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L11-6016 | Electrical RI | 5 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L11-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L12-6019 | Complete Top Out GWB | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L14-6020 | Install Hollow Metal Frames | 3 | 0 | 02-Jun-14 A | 05-Jun-14 A | |
| L14-6010 | Frame Walls | 5 | 0 | 02-Jun-14 A | 04-Jun-14 A | |
| L16-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| L14-6019 | Complete Top Out GWB | 2 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L16-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L10-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| L17-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 04-Jun-14 A | 11-Jun-14 A | |
| L08-6016 | Electrical RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L08-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L09-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L12-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L15-6010 | Frame Walls | 3 | 0 | 05-Jun-14 A | 11-Jun-14 A | |

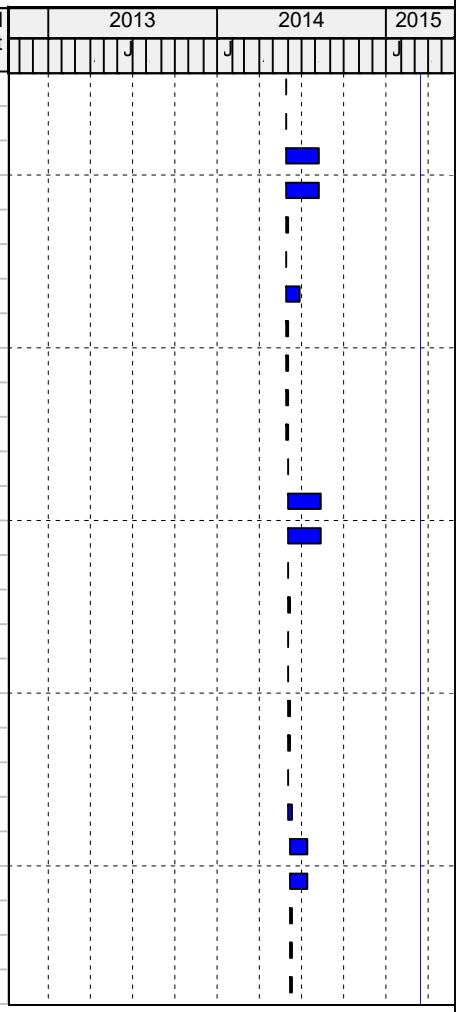



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6012 | Fire Sprinkler Mains | 5 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L09-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L11-6012 | Fire Sprinkler Mains | 4 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L12-6014 | Set Tubs & Plumbing Rl | 4 | 0 | 06-Jun-14 A | 27-Jun-14 A | |
| L11-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jun-14 A | 11-Jun-14 A | |
| L09-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 09-Jun-14 A | 25-Jun-14 A | |
| L14-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L15-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L16-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L09-6016 | Electrical Rl | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L14-6014 | Set Tubs & Plumbing Rl | 4 | 0 | 10-Jun-14 A | 21-Jul-14 A | |
| L15-6020 | Install Hollow Metal Frames | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L15-6019 | Complete Top Out GWB | 2 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6014 | Set Tubs & Plumbing Rl | 4 | 0 | 11-Jun-14 A | 26-Jun-14 A | |
| L11-6028 | PreRock at Heat Pumps | 2 | 0 | 13-Jun-14 A | 14-Jun-14 A | |
| L11-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 14-Jun-14 A | 14-Jun-14 A | |
| L14-6012 | Fire Sprinkler Mains | 2 | 0 | 16-Jun-14 A | 27-Jun-14 A | |
| L14-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 18-Jun-14 A | 18-Jun-14 A | |
| L15-6023 | Inspection of Exterior Framing | 0 | 0 | 18-Jun-14 A | | |
| L17-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 18-Jun-14 A | 23-Jun-14 A | |
| L17-6010 | Frame Walls | 5 | 0 | 18-Jun-14 A | 29-Jul-14 A | |
| L10-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L12-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-Jun-14 A | 19-Jun-14 A | |

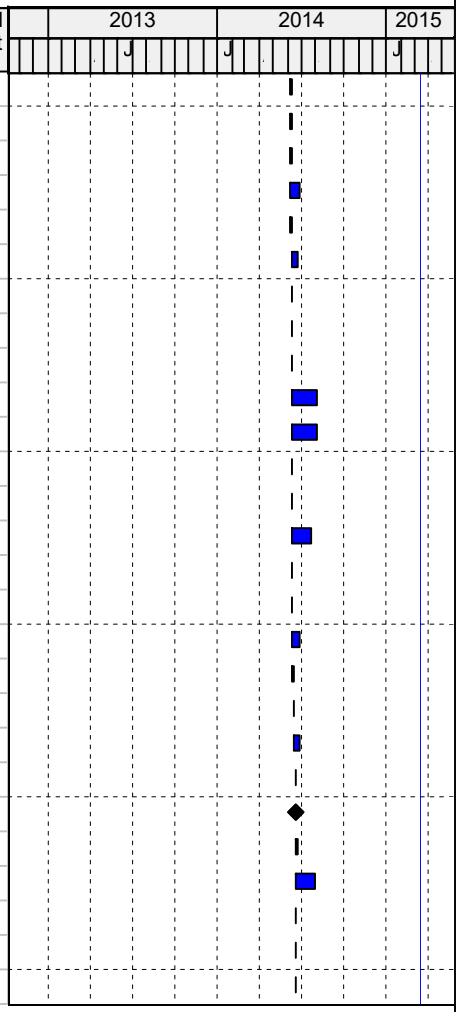


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6023 | Inspection of Exterior Framing | 0 | 0 | 20-Jun-14 A | | |
| L15-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-Jun-14 A | 20-Jun-14 A | |
| L10-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-Jun-14 A | 23-Jun-14 A | |
| L15-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 22-Jun-14 A | 24-Jul-14 A | |
| L08-6018 | HVAC Rl | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L12-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L14-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L15-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L08-6221 | Frame Unit Ceilings | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| L11-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 24-Jun-14 A | 27-Jun-14 A | |
| L12-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L14-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6023 | Inspection of Exterior Framing | 0 | 0 | 24-Jun-14 A | | |
| L12-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| L12-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L14-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L15-6012 | Fire Sprinkler Mains | 2 | 0 | 25-Jun-14 A | 22-Jul-14 A | |
| L16-6023 | Inspection of Exterior Framing | 0 | 0 | 25-Jun-14 A | | |
| L03-6024 | Inspections for GWB Cover | 1 | 0 | 27-Jun-14 A | 27-Jun-14 A | |
| L09-6018 | HVAC Rl | 3 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L09-6221 | Frame Unit Ceilings | 2 | 0 | 27-Jun-14 A | 30-Jun-14 A | |
| L12-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L14-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L15-6028 | PreRock at Heat Pumps | 2 | 0 | 30-Jun-14 A | 01-Jul-14 A | |
| L16-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 30-Jun-14 A | 30-Jun-14 A | |

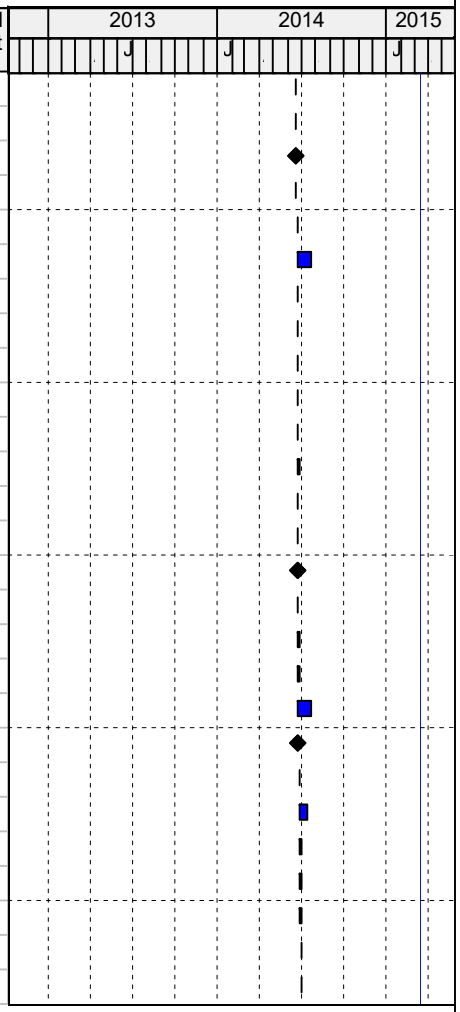


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6010 | Frame Walls | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| L16-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L15-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L15-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L04-6024 | Inspections for GWB Cover | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L10-6018 | HVAC RI | 3 | 0 | 07-Jul-14 A | 21-Jul-14 A | |
| L11-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L15-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L16-6012 | Fire Sprinkler Mains | 2 | 0 | 07-Jul-14 A | 24-Jul-14 A | |
| L16-6020 | Install Hollow Metal Frames | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L16-6028 | PreRock at Heat Pumps | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L17-6019 | Complete Top Out GWB | 1 | 0 | 07-Jul-14 A | 08-Aug-14 A | |
| L11-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L15-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 08-Jul-14 A | 04-Aug-14 A | |
| L17-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jul-14 A | 01-Aug-14 A | |
| L10-6221 | Frame Unit Ceilings | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| L17-6012 | Fire Sprinkler Mains | 2 | 0 | 09-Jul-14 A | 12-Aug-14 A | |
| L05-6024 | Inspections for GWB Cover | 2 | 0 | 10-Jul-14 A | 10-Jul-14 A | |
| L04-6000 | Tape/Finish GWB | 6 | 0 | 11-Jul-14 A | 23-Jul-14 A | |
| L16-6019 | Complete Top Out GWB | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L16-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L15-6018 | HVAC RI | 3 | 0 | 16-Jul-14 A | 18-Jul-14 A | |
| L16-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-6024 | Inspections for GWB Cover | 2 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6018 | HVAC RI | 3 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L16-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 21-Jul-14 A | 18-Aug-14 A | |

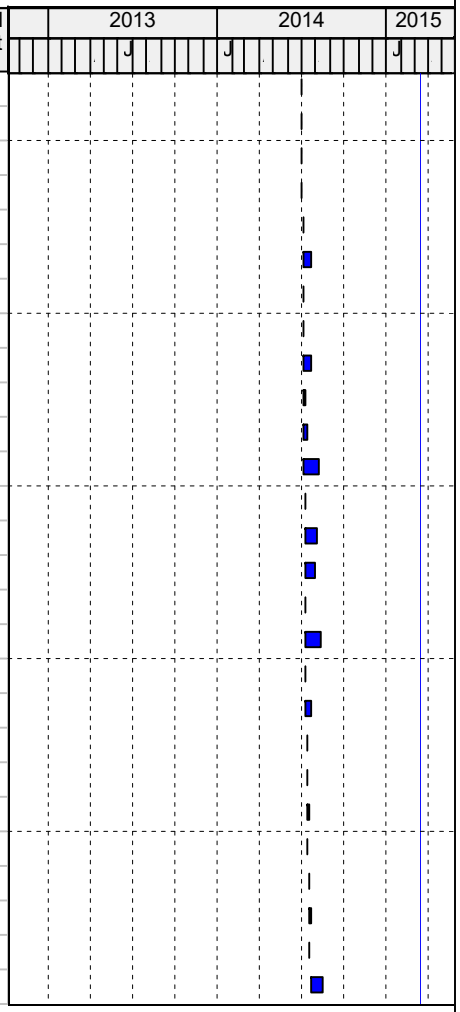



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6013 | Fire Sprinkler Branch Lines | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| L03-6000 | Tape/Finish GWB | 6 | 0 | 23-Jul-14 A | 29-Jul-14 A | |
| L11-6018 | HVAC RI | 3 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L15-6221 | Frame Unit Ceilings | 2 | 0 | 23-Jul-14 A | 01-Aug-14 A | |
| L16-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L17-6020 | Install Hollow Metal Frames | 3 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| L11-6221 | Frame Unit Ceilings | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L12-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L14-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L14-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L16-6014 | Set Tubs & Plumbing RI | 5 | 0 | 28-Jul-14 A | 18-Aug-14 A | |
| L07-6024 | Inspections for GWB Cover | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L12-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L05-6000 | Tape/Finish GWB | 6 | 0 | 31-Jul-14 A | 05-Aug-14 A | |
| L08-6024 | Inspections for GWB Cover | 2 | 0 | 31-Jul-14 A | 31-Jul-14 A | |
| L12-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L14-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L06-6000 | Tape/Finish GWB | 4 | 0 | 06-Aug-14 A | 11-Aug-14 A | |
| L09-6024 | Inspections for GWB Cover | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L07-6000 | Tape/Finish GWB | 5 | 0 | 07-Aug-14 A | 16-Aug-14 A | |
| L11-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 08-Aug-14 A | 14-Aug-14 A | |
| L17-6014 | Set Tubs & Plumbing RI | 5 | 0 | 08-Aug-14 A | 16-Sep-14 A | |

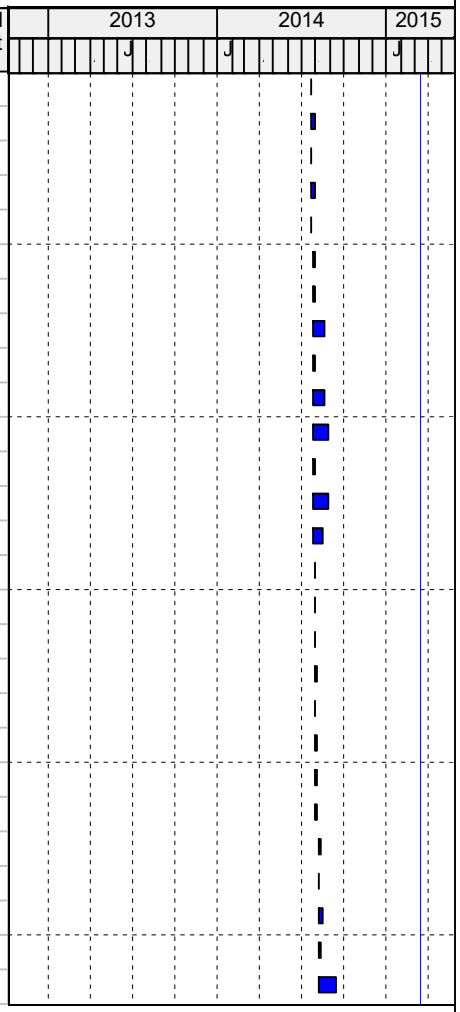



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-6024 | Inspections for GWB Cover | 2 | 0 | 11-Aug-14 A | 12-Aug-14 A | |
| L09-6000 | Tape/Finish GWB | 5 | 0 | 14-Aug-14 A | 19-Aug-14 A | |
| L08-6000 | Tape/Finish GWB | 5 | 0 | 16-Aug-14 A | 21-Aug-14 A | |
| L11-6024 | Inspections for GWB Cover | 2 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L16-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 18-Aug-14 A | 29-Aug-14 A | |
| L10-6000 | Tape/Finish GWB | 5 | 0 | 19-Aug-14 A | 23-Aug-14 A | |
| L16-6221 | Frame Unit Ceilings | 4 | 0 | 21-Aug-14 A | 26-Aug-14 A | |
| L17-6018 | HVAC RI | 3 | 0 | 21-Aug-14 A | 10-Sep-14 A | |
| L12-6024 | Inspections for GWB Cover | 2 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L15-6016 | Electrical RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L15-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L11-6000 | Tape/Finish GWB | 5 | 0 | 23-Aug-14 A | 29-Aug-14 A | |
| L17-6221 | Frame Unit Ceilings | 4 | 0 | 26-Aug-14 A | 28-Aug-14 A | |
| L14-6024 | Inspections for GWB Cover | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L16-6016 | Electrical RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L16-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L12-6000 | Tape/Finish GWB | 5 | 0 | 02-Sep-14 A | 08-Sep-14 A | |
| L15-6024 | Inspections for GWB Cover | 2 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L14-6000 | Tape/Finish GWB | 5 | 0 | 06-Sep-14 A | 11-Sep-14 A | |
| L15-6000 | Tape/Finish GWB | 4 | 0 | 12-Sep-14 A | 20-Sep-14 A | |
| L17-6016 | Electrical RI | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-6028 | PreRock at Heat Pumps | 2 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L17-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L17-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |

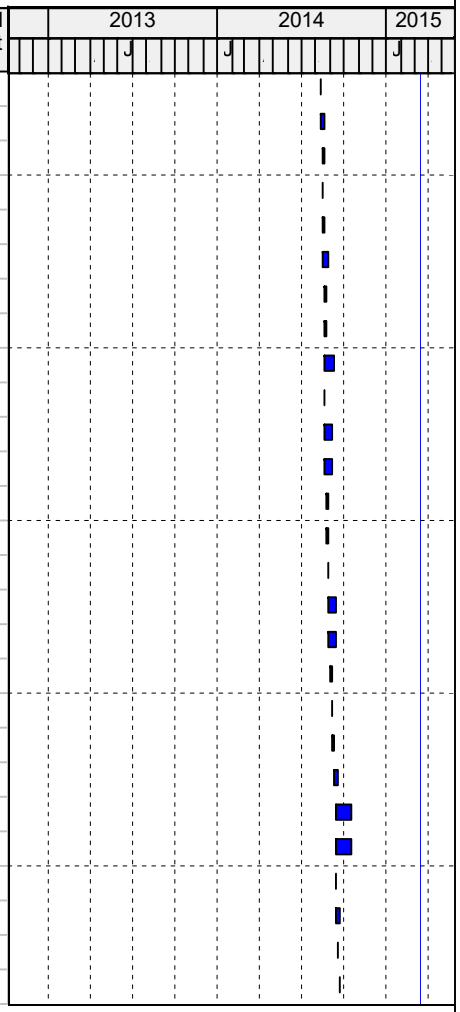



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L17-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 24-Sep-14 A | 27-Sep-14 A | |
| L17-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L16-6024 | Inspections for GWB Cover | 1 | 0 | 08-Oct-14 A | 09-Oct-14 A | |
| L16-6000 | Tape/Finish GWB | 4 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6024 | Inspections for GWB Cover | 1 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6000 | Tape/Finish GWB | 6 | 0 | 30-Oct-14 A | 07-Nov-14 A | |
| **Mechanical Penthouse** | | | | | | |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 0 | 11-Jun-14 A | 20-Jun-14 A | |
| PH-6006 | PH - Exterior Wall Framing (including PH roof parapet | 6 | 0 | 12-Jun-14 A | 14-Jul-14 A | |
| PH-6014 | PH - Plumbing/Piping RI | 40 | 0 | 25-Jun-14 A | 05-Nov-14 A | |
| PH-6002 | PH - Layout | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| PH-6008 | PH - Interior Wall Framing | 3 | 0 | 24-Jul-14 A | 08-Aug-14 A | |
| PH-6020 | PH - H Mtl Frames | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| PH-6012 | PH - Fire Sprinkler RI | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |
| PH-6018 | PH - HVAC RI | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |
| PH-6016 | PH - Electrical RI | 10 | 0 | 23-Sep-14 A | 14-Nov-14 A | |
| PH-6022 | PH - Fire Alarm / Elec Specialties RI | 10 | 0 | 23-Sep-14 A | 14-Nov-14 A | |
| **Finishes** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL4-8100 | LL4 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| LL4-8102 | LL4 - GWB Hang (incl. screw inspection) | 3 | 0 | 27-Oct-14 A | 10-Dec-14 A | |
| LL4-8114 | LL4 - Striping / Signage (DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL4-8104 | LL4 - Int Painting | 3 | 0 | 22-Dec-14 A | 24-Dec-14 A | |

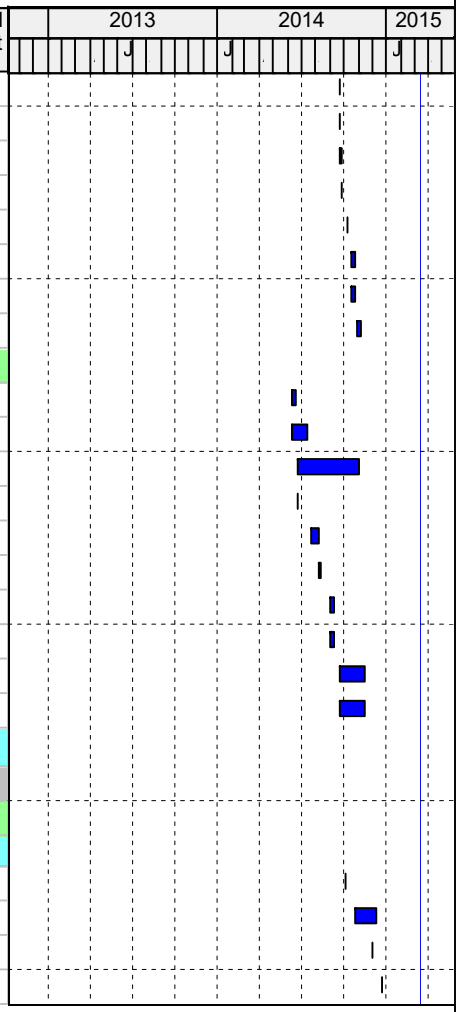



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8122 | LL4 - Plumbing Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL4-8108 | Electrical trim & finish | 5 | 0 | 29-Dec-14 A | 16-Feb-15 A | |
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL4-8126 | Install doors & hardware | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL4-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 22-Jan-15 A | 26-Jan-15 A | |
| LL4-8124 | Flooring - VCT | 4 | 0 | 05-Feb-15 A | 06-Feb-15 A | |
| LL4-8110 | HVAC trim | 2 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| LL4-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 06-Apr-15 | 10-Apr-15 | 15 |
| LL4-8134 | Final Cleaning | 2 | 2 | 10-Apr-15 | 13-Apr-15 | 15 |
| LL4-8214 | Floor Complete | 0 | 0 | | 13-Apr-15 | 15 |
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL3-8100 | LL3 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| LL3-8102 | LL3 - GWB Hang (incl. screw inspection) | 3 | 0 | 27-Oct-14 A | 10-Dec-14 A | |
| LL3-8114 | LL3 - Striping / Signage [DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL3-8104 | LL3 - Int Painting | 3 | 0 | 22-Dec-14 A | 24-Dec-14 A | |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL3-8108 | Electrical trim & finish | 5 | 0 | 29-Dec-14 A | 16-Feb-15 A | |
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL3-8126 | Install doors & hardware | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL3-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 22-Jan-15 A | 03-Feb-15 A | |
| LL3-8124 | Flooring - VCT | 4 | 0 | 06-Feb-15 A | 07-Feb-15 A | |
| LL3-8110 | HVAC trim | 2 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| LL3-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 06-Apr-15 | 10-Apr-15 | 15 |
| LL3-8134 | Final Cleaning | 2 | 2 | 10-Apr-15 | 13-Apr-15 | 15 |
| LL3-8214 | Floor Complete | 0 | 0 | | 13-Apr-15 | 15 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |

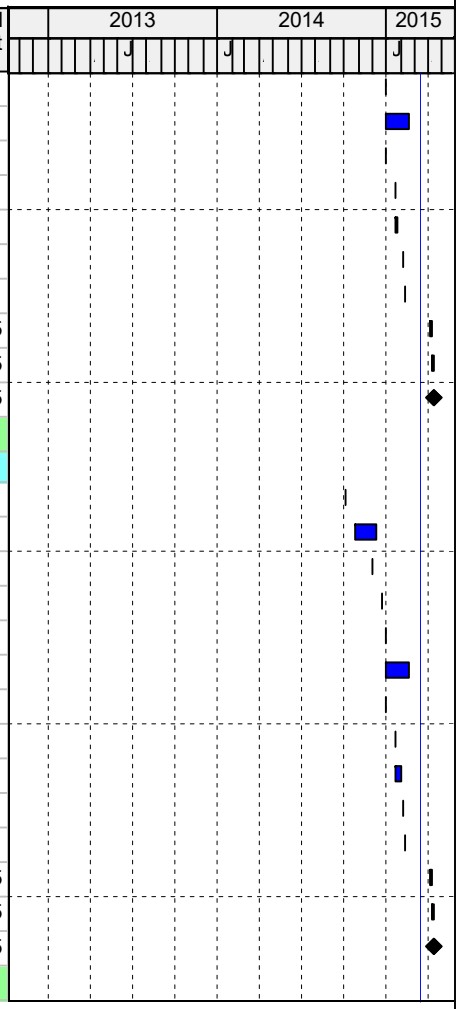



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Corridors / Common / Public Areas** | | | | | | |
| LL2E-8102 | LL2 - GWB Hang / Tape / Finish @ Electrical Rooms | 8 | 0 | 24-Jun-14 A | 03-Jul-14 A | |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish & Inspection | 6 | 0 | 16-Sep-14 A | 22-Dec-14 A | |
| LL2-8100 | LL2 - Insulation | 5 | 0 | 16-Sep-14 A | 09-Oct-14 A | |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 5 | 0 | 17-Sep-14 A | 27-Oct-14 A | |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| LL2-8104 | LL2 - Int Painting | 5 | 0 | 25-Nov-14 A | 23-Dec-14 A | |
| LL2-8114 | LL2 - Striping / Signage [DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL2-8116 | LL2 - Finish Carpentry / Millwork [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL2-8124 | Flooring - VCT | 4 | 0 | 06-Feb-15 A | 10-Mar-15 A | |
| LL2-8126 | Install doors & hardware | 3 | 0 | 09-Feb-15 A | 16-Feb-15 A | |
| LL2-8128 | Entry Gates at Garage | 5 | 5 | 30-Mar-15 | 03-Apr-15 | 26 |
| LL2-8136 | Chainlink Fencing / Gate @ Recycling at Garage | 5 | 5 | 30-Mar-15 | 03-Apr-15 | 26 |
| LL2-8120 | Install bollards at Garage | 5 | 5 | 30-Mar-15 | 03-Apr-15 | 26 |
| LL2-8122 | Complete MEP trim | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 4 |
| LL2-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 22-Apr-15 | 28-Apr-15 | 8 |
| LL2-8134 | Final Cleaning | 2 | 2 | 28-Apr-15 | 29-Apr-15 | 8 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 31-Jul-14 A | |
| LL1-Z2U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 09-May-14 A | |
| LL1-Z3U-8102 | Above Ceiling GWB (At All Areas North of Q-Line) | 5 | 0 | 10-Feb-14 A | 20-Jun-14 A | |
| L1BU-8102 | Above Ceiling GWB [including East Service Corridor] | 5 | 0 | 06-Jun-14 A | 11-Jun-14 A | |
| L1LU-8102 | Above Ceiling GWB | 5 | 0 | 24-Jun-14 A | 13-Oct-14 A | |
| L1KU-8102 | Above Ceiling GWB | 2 | 0 | 26-Jun-14 A | 22-Aug-14 A | |
| LL1-8100 | Insulation | 5 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| LL1-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 28-Jul-14 A | 06-Aug-14 A | |

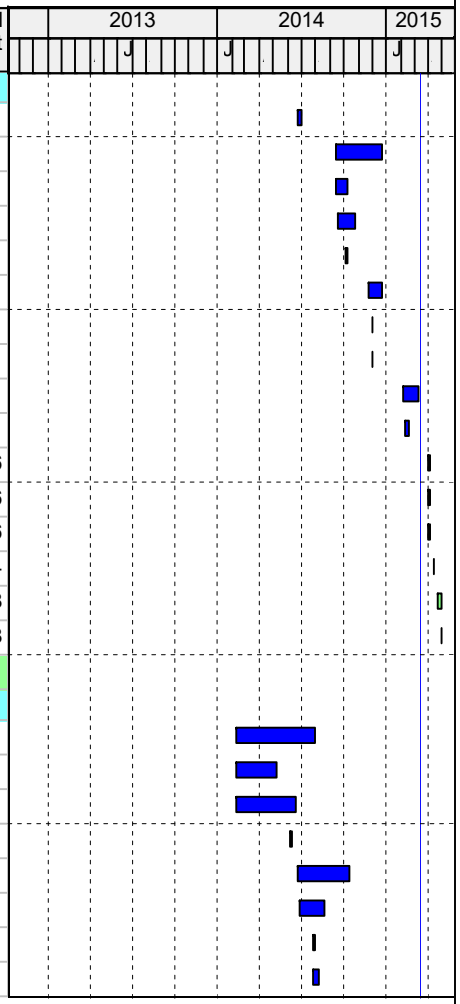


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-8102 | GWB Hang (Walls) & Inspection | 4 | 0 | 11-Aug-14 A | 14-Aug-14 A | |
| LL1-Z2-8100 | Insulation | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| LL1-8215 | GWB Tape (Walls) | 10 | 0 | 16-Aug-14 A | 07-Nov-14 A | |
| LL1-Z3-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 15-Sep-14 A | 07-Oct-14 A | |
| LL1-Z3-8100 | Insulation | 5 | 0 | 15-Sep-14 A | 24-Sep-14 A | |
| LL1-Z2-8215 | GWB Tape (Walls/Ceilings) | 7 | 0 | 29-Sep-14 A | 07-Nov-14 A | |
| L1B-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L1K-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| LL1-Z3-8215 | GWB Tape (Walls & Ceilings) | 7 | 0 | 07-Oct-14 A | 18-Nov-14 A | |
| L1K-8102 | GWB Hang (Walls) & Inspection | 8 | 0 | 09-Oct-14 A | 31-Oct-14 A | |
| L1L-8100 | Insulation | 4 | 0 | 13-Oct-14 A | 16-Oct-14 A | |
| L1B-8102 | GWB Hang (Walls) & Inspection - Main Ballroom N/S/ | 4 | 0 | 16-Oct-14 A | 22-Oct-14 A | |
| L1L-8102 | GWB hang walls (Dining & Lounge) | 4 | 0 | 30-Oct-14 A | 05-Feb-15 A | |
| L1K-8215 | GWB Tape (Walls & Ceilings) | 4 | 0 | 05-Nov-14 A | 18-Nov-14 A | |
| LL1-Z3-8104 | Prime Paint | 4 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| LL1-8104 | Prime Paint & First Coat Finish Paint | 5 | 0 | 02-Dec-14 A | 12-Dec-14 A | |
| L1K-8106 | Wall coverings - FRP | 8 | 0 | 19-Dec-14 A | 08-Jan-15 A | |
| LL1-Z3-8114 | Ceiling grid & inspection | 4 | 0 | 13-Jan-15 A | 16-Jan-15 A | |
| LL1-8126 | Install doors & hardware | 5 | 0 | 26-Jan-15 A | 03-Feb-15 A | |
| L1L-8215 | GWB hang ceilings (Dining & Lounge) | 5 | 0 | 29-Jan-15 A | 05-Feb-15 A | |
| LL1-8116 | Finish carpentry/millwork | 10 | 0 | 05-Feb-15 A | 02-Mar-15 A | |
| L1K-8114 | Ceiling grid & inspection (east end) | 8 | 0 | 05-Feb-15 A | 13-Mar-15 A | |
| LL1-Z3-8126 | Install doors & hardware | 5 | 0 | 09-Feb-15 A | 12-Feb-15 A | |
| L1K-8124 | Flooring - VCT | 3 | 2 | 10-Feb-15 A | 30-Mar-15 | 11 |
| LL1-8114 | Ceiling grid & inspection | 4 | 0 | 11-Feb-15 A | 20-Feb-15 A | |
| LL1-8118 | Lighting & electrical drops to grid | 3 | 0 | 12-Feb-15 A | 20-Feb-15 A | |
| LL1-Z2-8104 | Paint, prime at Jr. Ballrooms | 2 | 0 | 12-Feb-15 A | 13-Feb-15 A | |

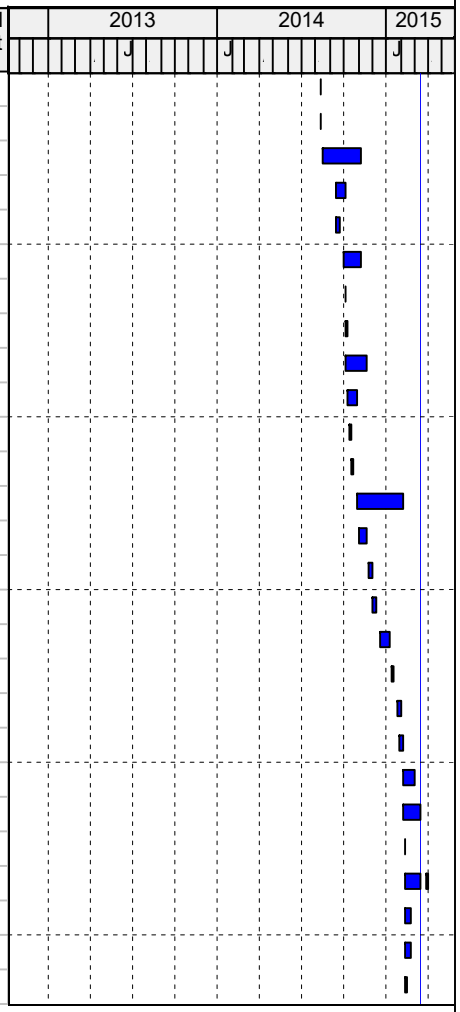



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8104 | Paint, prime | 2 | 0 | 13-Feb-15 A | 17-Feb-15 A | |
| LL1-Z2-8126 | Install doors & hardware | 3 | 1 | 16-Feb-15 A | 16-Mar-15 | 47 |
| LL1-8112 | Fire sprinkler drops to grid | 2 | 0 | 17-Feb-15 A | 20-Feb-15 A | |
| LL1-Z2-8106 | Wall coverings - vinyl at Jr. Ballrooms | 2 | 0 | 18-Feb-15 A | 19-Feb-15 A | |
| LL1-Z2-8114 | Ceiling grid & inspection | 5 | 0 | 18-Feb-15 A | 26-Feb-15 A | |
| L1L-8114 | Install 9-wood ceiling supports - north of Grid K | 3 | 0 | 19-Feb-15 A | 26-Feb-15 A | |
| LL1-Z2-8116 | Finish carpentry/millwork | 10 | 0 | 20-Feb-15 A | 02-Mar-15 A | |
| L1K-8104 | Paint, prime | 2 | 0 | 26-Feb-15 A | 27-Feb-15 A | |
| L1B-8104 | Paint, prime & first coat finish | 3 | 0 | 06-Mar-15 A | 10-Mar-15 A | |
| LL1-Z2-8124 | Flooring - VCT at service corridor | 2 | 0 | 09-Mar-15 A | 11-Mar-15 A | |
| LL1-Z3-8124 | Flooring - epoxy at Food Prep (including prep) | 6 | 0 | 09-Mar-15 A | 13-Mar-15 A | |
| LL1-8124 | Flooring - VCT at storage areas, janitorial, mechanica | 3 | 3 | 16-Mar-15 | 18-Mar-15 | 14 |
| L1L-8126 | Install doors & hardware | 4 | 4 | 16-Mar-15 | 19-Mar-15 | 4 |
| LL1-Z3-8118 | Lighting & electrical drops at ceiling | 3 | 3 | 17-Mar-15 | 19-Mar-15 | 11 |
| LL1-Z2-8118 | Lighting & electrical drops to grid | 3 | 3 | 18-Mar-15 | 20-Mar-15 | 17 |
| L1L-8140 | Install 9-wood ceiling - north of Grid K | 4 | 4 | 18-Mar-15 | 23-Mar-15 | 0 |
| L1L-8116 | Finish carpentry/millwork - north of Grid K | 5 | 5 | 19-Mar-15 | 25-Mar-15 | 1 |
| L1K-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 19-Mar-15 | 20-Mar-15 | 18 |
| LL1-Z3-8112 | Fire sprinkler drops/trim at ceiling | 2 | 2 | 20-Mar-15 | 23-Mar-15 | 11 |
| LL1-Z2-8112 | Fire sprinkler drops to grid | 2 | 2 | 23-Mar-15 | 24-Mar-15 | 17 |
| L1K-8112 | Fire sprinkler trim | 1 | 1 | 23-Mar-15 | 23-Mar-15 | 18 |
| LL1-Z3-8116 | Finish carpentry/millwork | 3 | 3 | 27-Mar-15 | 31-Mar-15 | 12 |
| L1L-8112 | Fire sprinkler trim - north of Grid K | 1 | 1 | 27-Mar-15 | 27-Mar-15 | 1 |
| L1L-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 1 | 27-Mar-15 | 27-Mar-15 | 1 |
| L1L-8124 | Flooring - wood - north of Grid K | 5 | 5 | 30-Mar-15 | 03-Apr-15 | 1 |
| L1L-8106 | Wall coverings - vinyl | 5 | 5 | 30-Mar-15 | 03-Apr-15 | 11 |
| L1B-8126 | Install doors & hardware at Ballrooms | 2 | 2 | 31-Mar-15 | 01-Apr-15 | 5 |

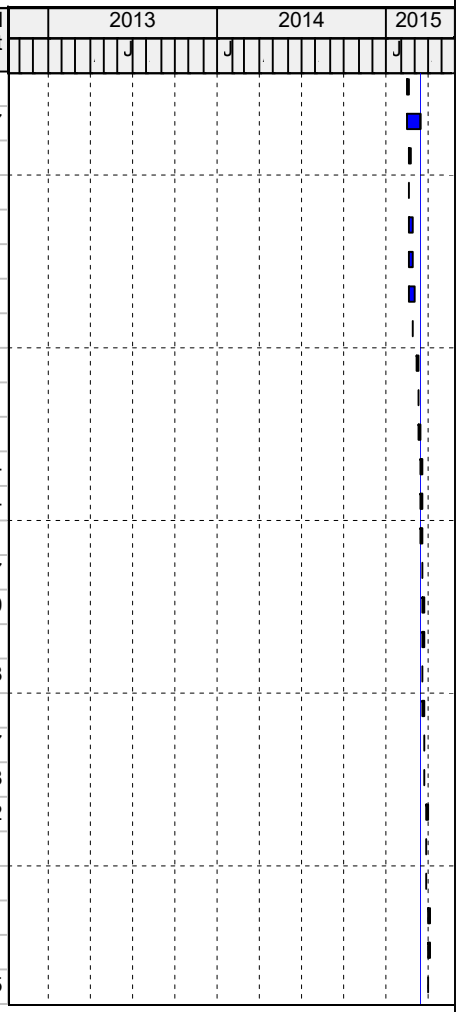



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8116 | Finish carpentry/millwork | 2 | 2 | 31-Mar-15 | 01-Apr-15 | 11 |
| L1K-8126 | Install doors & hardware | 3 | 3 | 31-Mar-15 | 02-Apr-15 | 8 |
| LL1-Z3-8140 | Complete acoustical ceiling tile | 2 | 2 | 01-Apr-15 | 02-Apr-15 | 12 |
| L1B-8116 | Finish carpentry/millwork at Ballrooms | 10 | 10 | 02-Apr-15 | 15-Apr-15 | 5 |
| L1B-8114 | Ceiling grid & inspection | 3 | 3 | 03-Apr-15 | 07-Apr-15 | 2 |
| LL1-Z2-8140 | Complete acoustical ceiling tile | 2 | 2 | 07-Apr-15 | 08-Apr-15 | 8 |
| LL1-Z3-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 4 | 4 | 10-Apr-15 | 15-Apr-15 | 12 |
| LL1-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 4 | 4 | 13-Apr-15 | 16-Apr-15 | 11 |
| LL1-Z3-8134 | Final Cleaning | 2 | 2 | 15-Apr-15 | 16-Apr-15 | 12 |
| LL1-8134 | Final Cleaning | 2 | 2 | 16-Apr-15 | 17-Apr-15 | 11 |
| LL1-Z2-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 4 | 4 | 16-Apr-15 | 21-Apr-15 | 8 |
| L1B-8124 | Flooring - carpet at Ballrooms | 4 | 4 | 16-Apr-15 | 21-Apr-15 | 0 |
| L1K-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 4 | 4 | 16-Apr-15 | 21-Apr-15 | 13 |
| LL1-Z2-8134 | Final Cleaning | 2 | 2 | 21-Apr-15 | 22-Apr-15 | 8 |
| L1K-8134 | Final Cleaning | 2 | 2 | 21-Apr-15 | 22-Apr-15 | 13 |
| L1B-8140 | Complete acoustical ceiling tile | 2 | 2 | 22-Apr-15 | 23-Apr-15 | 0 |
| L1B-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 4 | 4 | 01-May-15 | 06-May-15 | 7 |
| L1L-8132 | Owner Punchlist (inspect/distribute/correct/back-puncl | 4 | 4 | 01-May-15 | 06-May-15 | 7 |
| L1B-8134 | Final Cleaning | 2 | 2 | 06-May-15 | 07-May-15 | 7 |
| L1L-8134 | Final Cleaning | 2 | 2 | 06-May-15 | 07-May-15 | 7 |
| **Corridors / Common / Public Areas** | | | | | | |
| LL1-8200 | Wall coverings - vinyl | 4 | 0 | 17-Dec-14 A | 19-Jan-15 A | |
| LL1-Z3-8200 | Paint, first coat finish | 4 | 0 | 07-Jan-15 A | 12-Jan-15 A | |
| LL1-Z3-8204 | HVAC drops/trim at ceiling | 2 | 1 | 02-Feb-15 A | 16-Mar-15 | 11 |
| LL1-8204 | HVAC drops/trim to grid | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| LL1-Z2-8200 | Paint, first coat finish at Jr. Ballrooms | 1 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| L1L-8200 | Paint, first coat finish | 2 | 0 | 18-Feb-15 A | 18-Feb-15 A | |

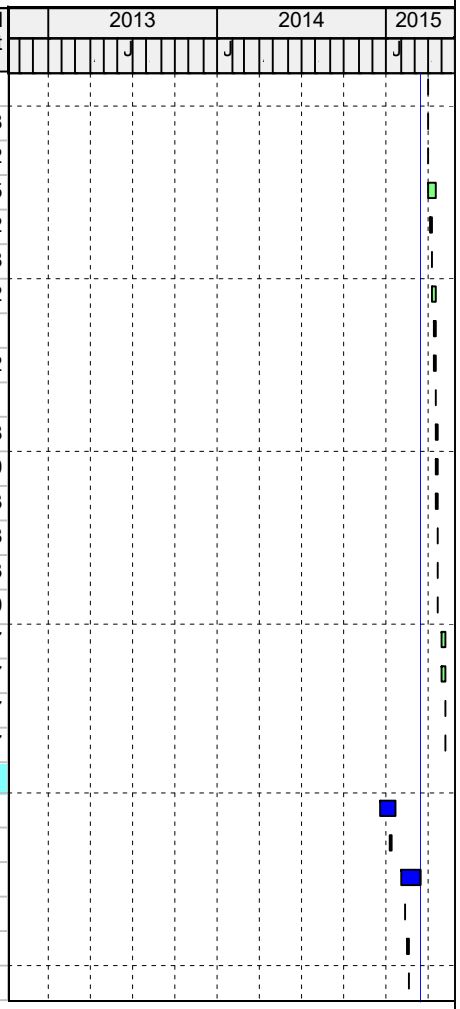



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8200 | Paint, first coat finish | 1 | 0 | 02-Mar-15 A | 02-Mar-15 A | |
| LL1-Z2-8204 | HVAC drops/trim to grid | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 17 |
| L1K-8204 | HVAC drops/trim at ceiling | 1 | 1 | 19-Mar-15 | 19-Mar-15 | 8 |
| L1L-8204 | HVAC trim at ceiling - north of Grid K | 1 | 1 | 24-Mar-15 | 24-Mar-15 | 1 |
| L1B-8200 | Paint ceiling clouds | 3 | 3 | 26-Mar-15 | 30-Mar-15 | 0 |
| LL1-Z3-8214 | LL1, Zone 3 Complete | 0 | 0 | | 16-Apr-15 | 12 |
| LL1-8214 | LL1, Zone 1 Complete | 0 | 0 | | 17-Apr-15 | 11 |
| L1B-8201 | Complete paint final coat & touch-up | 2 | 2 | 22-Apr-15 | 23-Apr-15 | 0 |
| LL1-Z2-8214 | LL1 Zone 2 Complete | 0 | 0 | | 22-Apr-15 | 8 |
| L1K-8214 | L1, Zone 1 Complete | 0 | 0 | | 22-Apr-15 | 13 |
| L1B-8214 | L1, Zone 2 Complete | 0 | 0 | | 07-May-15 | 7 |
| L1L-8214 | L1, Zone 4 Complete | 0 | 0 | | 07-May-15 | 7 |
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8100 | L2 - Insulation - North Half | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L02-8102 | L2 - GWB Hang / Tape / Finish - North Half | 7 | 0 | 23-Oct-14 A | 17-Dec-14 A | |
| L02-8104 | Paint, prime & first coat finish at north half | 3 | 3 | 16-Mar-15 | 18-Mar-15 | 6 |
| L02-8106 | Wall coverings - vinyl at south half | 4 | 4 | 16-Mar-15 | 19-Mar-15 | 9 |
| L02-8126 | Install doors & hardware at south half | 5 | 5 | 20-Mar-15 | 26-Mar-15 | 9 |
| L02-8110 | HVAC drops/trim at south half | 2 | 2 | 24-Mar-15 | 25-Mar-15 | 6 |
| L02-8120 | Ceramic tile | 3 | 3 | 25-Mar-15 | 27-Mar-15 | 7 |
| L02-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 26-Mar-15 | 27-Mar-15 | 6 |
| L02-8112 | Fire sprinkler drops/trim at south half | 2 | 2 | 30-Mar-15 | 31-Mar-15 | 12 |
| L02-8122 | Plumbing fixtures & trim | 4 | 4 | 01-Apr-15 | 06-Apr-15 | 5 |
| L02-8124 | Flooring - carpet | 4 | 4 | 01-Apr-15 | 06-Apr-15 | 6 |
| L02-8116 | Finish carpentry/millwork at south half | 2 | 2 | 07-Apr-15 | 08-Apr-15 | 6 |
| L02-8128 | Install bathroom accessories | 3 | 3 | 07-Apr-15 | 09-Apr-15 | 5 |

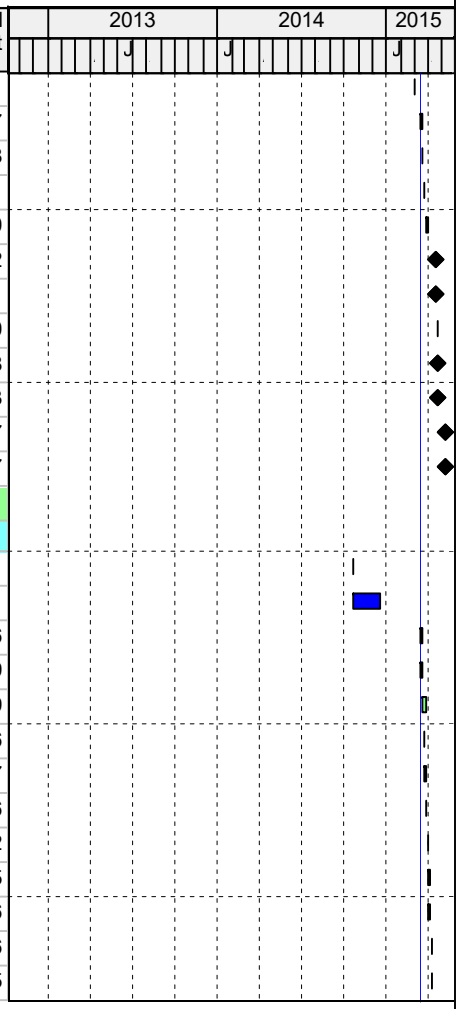



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8136 | Lockers / Benches @ Locker Rooms | 3 | 3 | 07-Apr-15 | 09-Apr-15 | 5 |
| L02-8108 | Complete MEP trim | 2 | 2 | 10-Apr-15 | 13-Apr-15 | 5 |
| L02-8132 | Owner Punchlist (inspect/distribute/correct/back-punch | 3 | 3 | 21-Apr-15 | 23-Apr-15 | 11 |
| L02-8134 | Final Cleaning | 2 | 2 | 23-Apr-15 | 24-Apr-15 | 11 |
| **Corridors** | | | | | | |
| L02-8200 | Complete paint final coat & touch-up | 2 | 2 | 10-Apr-15 | 13-Apr-15 | 5 |
| L02-8214 | Floor Complete | 0 | 0 | | 24-Apr-15 | 11 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L03-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L04-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L05-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L06-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L07-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L08-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L09-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L10-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L11-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L12-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L14-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L15-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L16-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L17-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L03-8102S | Stock GWB | 2 | 0 | 27-Jun-14 A | 08-Jul-14 A | |
| L04-8102 | Hang GWB & Inspection | 4 | 0 | 07-Jul-14 A | 16-Jul-14 A | |
| L04-8102S | Stock GWB | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |

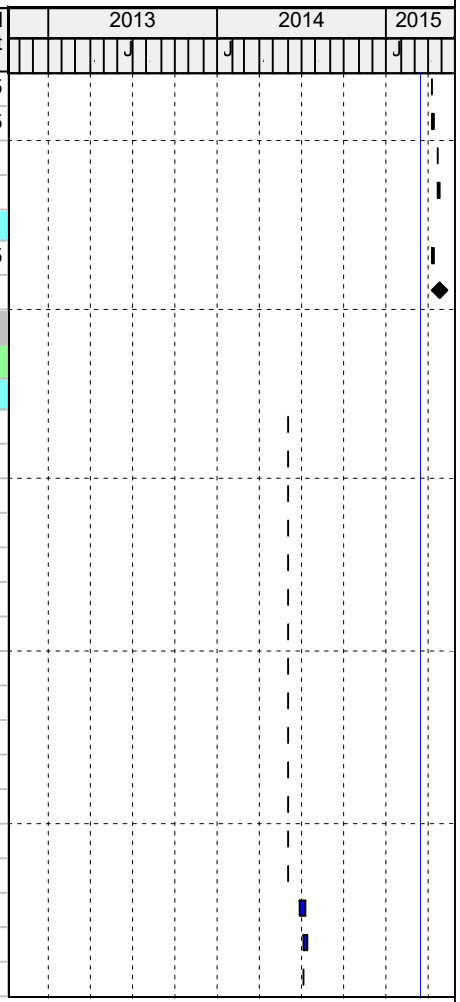



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8102 | Hang GWB & Inspection | 5 | 0 | 09-Jul-14 A | 22-Jul-14 A | |
| L05-8102S | Stock GWB | 2 | 0 | 10-Jul-14 A | 14-Jul-14 A | |
| L05-8102 | Hang GWB & Inspection | 4 | 0 | 17-Jul-14 A | 23-Jul-14 A | |
| L06-8102S | Stock GWB | 2 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L04-8104 | Paint (Prime) | 2 | 0 | 28-Jul-14 A | 05-Aug-14 A | |
| L03-8104 | Paint (Prime) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L03-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L07-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L08-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L06-8102 | Hang GWB & Inspection | 5 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L07-8102 | Hang GWB & Inspection | 6 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L04-8105 | Paint (First Coat & Ceilings) | 5 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L05-8104 | Paint (Prime) | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| L09-8102S | Stock GWB | 2 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 07-Aug-14 A | 11-Aug-14 A | |
| L09-8102 | Hang GWB & Inspection | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| L08-8102 | Hang GWB & Inspection | 6 | 0 | 11-Aug-14 A | 15-Aug-14 A | |
| L06-8104 | Paint (Prime) | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L10-8102S | Stock GWB | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-8102 | Hang GWB & Inspection | 4 | 0 | 13-Aug-14 A | 18-Aug-14 A | |
| L06-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 14-Aug-14 A | 18-Aug-14 A | |
| L11-8102S | Stock GWB | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L07-8104 | Paint (Prime) | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L11-8102 | Hang GWB & Inspection | 4 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| L07-8105 | Paint (First Coat & Ceilings) | 4 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L09-8104 | Paint (Prime) | 2 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L08-8104 | Paint (Prime) | 2 | 0 | 22-Aug-14 A | 25-Aug-14 A | |

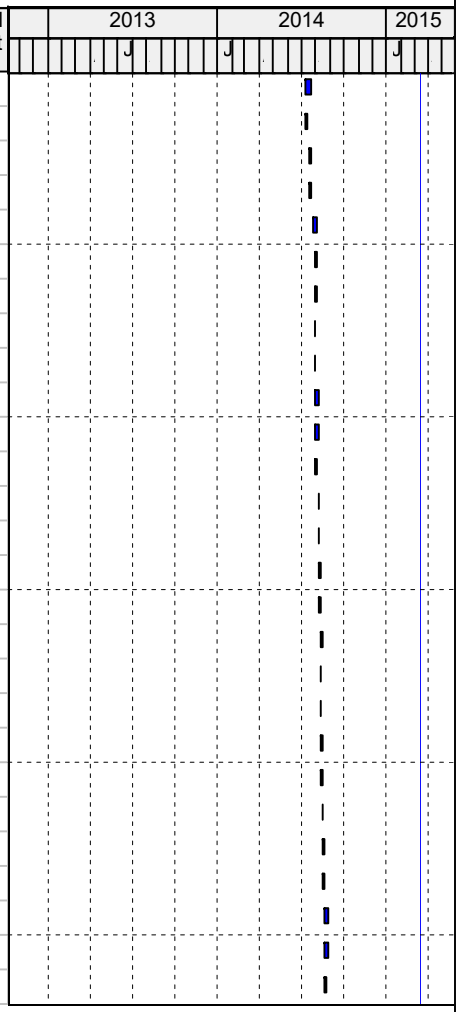



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8102 | Hang GWB & Inspection | 4 | 0 | 22-Aug-14 A | 30-Aug-14 A | |
| L12-8102S | Stock GWB | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8108 | Elec Trim / Finish | 4 | 0 | 25-Aug-14 A | 04-Sep-14 A | |
| L08-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L03-8118 | Fire Alarm Trim / Finish | 3 | 0 | 27-Aug-14 A | 29-Sep-14 A | |
| L14-8102S | Stock GWB | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L09-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 29-Aug-14 A | 09-Sep-14 A | |
| L14-8102 | Hang GWB & Inspection | 5 | 0 | 29-Aug-14 A | 05-Sep-14 A | |
| L03-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 02-Sep-14 A | 05-Sep-14 A | |
| L04-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 04-Sep-14 A | 09-Sep-14 A | |
| L10-8104 | Paint (Prime) | 2 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| L15-8102S | Stock GWB | 1 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L15-8102 | Hang GWB & Inspection | 5 | 0 | 06-Sep-14 A | 12-Sep-14 A | |
| L03-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8108 | Elec Trim / Finish | 4 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L04-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 11-Sep-14 A | |
| L05-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 08-Sep-14 A | 12-Sep-14 A | |
| L10-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 08-Sep-14 A | 12-Sep-14 A | |
| L11-8104 | Paint (Prime) | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L04-8116 | Install Base at Guestrooms | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L11-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 10-Sep-14 A | 22-Sep-14 A | |
| L03-8116 | Install Base at Guestrooms | 5 | 0 | 12-Sep-14 A | 16-Sep-14 A | |
| L12-8104 | Paint (Prime) | 2 | 0 | 12-Sep-14 A | 17-Sep-14 A | |
| L05-8116 | Install Base at Guestrooms | 5 | 0 | 16-Sep-14 A | 24-Sep-14 A | |
| L06-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L05-8108 | Elec Trim / Finish | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |

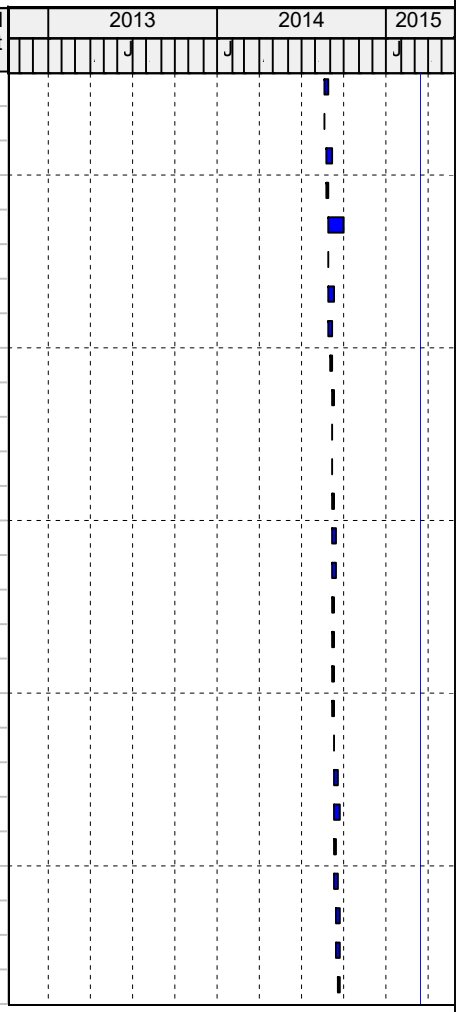



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 17-Sep-14 A | 23-Sep-14 A | |
| L12-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 17-Sep-14 A | 06-Oct-14 A | |
| L06-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L07-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L14-8104 | Paint (Prime) | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L06-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L06-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L08-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L14-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 24-Sep-14 A | 06-Oct-14 A | |
| L15-8104 | Paint (Prime) | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L03-8110 | HVAC Grilles & Registers | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L03-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8118 | Fire Alarm Trim / Finish | 3 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L10-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L08-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 30-Sep-14 A | 06-Oct-14 A | |
| L03-8126 | Install Doors | 3 | 0 | 01-Oct-14 A | 07-Oct-14 A | |
| L03-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 01-Oct-14 A | 28-Oct-14 A | |
| L04-8126 | Install Doors | 3 | 0 | 02-Oct-14 A | 09-Oct-14 A | |
| L08-8116 | Install Base at Guestrooms | 5 | 0 | 02-Oct-14 A | 08-Oct-14 A | |
| L04-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8118 | Fire Alarm Trim / Finish | 3 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8108 | Elec Trim / Finish | 4 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L15-8105 | Paint - First Coast & Ceilings | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |

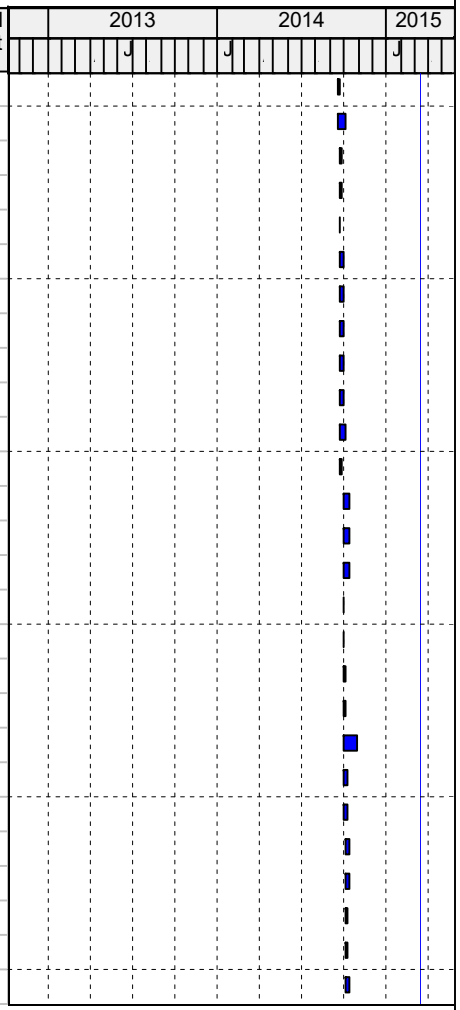


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8126 | Install Doors | 3 | 0 | 08-Oct-14 A | 10-Oct-14 A | |
| L09-8116 | Install Base and Door Thresholds | 5 | 0 | 08-Oct-14 A | 15-Oct-14 A | |
| L09-8124 | Install Flooring | 5 | 0 | 08-Oct-14 A | 14-Oct-14 A | |
| L16-8102S | Stock GWB | 1 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L09-8112 | Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 10-Oct-14 A | |
| L16-8102 | Hang GWB & Inspection | 4 | 0 | 10-Oct-14 A | 17-Oct-14 A | |
| L06-8118 | Fire Alarm Trim / Finish | 3 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L09-8108 | Lighting and Electrical Trim | 3 | 0 | 13-Oct-14 A | 15-Oct-14 A | |
| L10-8124 | Install Flooring | 5 | 0 | 13-Oct-14 A | 16-Oct-14 A | |
| L11-8112 | Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L03-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 14-Oct-14 A | 04-Nov-14 A | |
| L06-8110 | HVAC Grilles & Registers | 2 | 0 | 14-Oct-14 A | 21-Oct-14 A | |
| L06-8126 | Install Doors | 2 | 0 | 14-Oct-14 A | 20-Oct-14 A | |
| L07-8118 | Fire Alarm Trim / Finish | 3 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L12-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L14-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L08-8118 | Fire Alarm Trim / Finish | 3 | 0 | 15-Oct-14 A | 16-Oct-14 A | |
| L10-8116 | Install Base and Door Thresholds | 5 | 0 | 15-Oct-14 A | 23-Oct-14 A | |
| L15-8112 | Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 16-Oct-14 A | |
| L04-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 16-Oct-14 A | 11-Nov-14 A | |
| L11-8124 | Install Flooring | 5 | 0 | 16-Oct-14 A | 22-Oct-14 A | |
| L17-8102S | Stock GWB | 1 | 0 | 17-Oct-14 A | 17-Oct-14 A | |
| L07-8126 | Install Doors | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |
| L09-8118 | Fire Alarm Trim | 2 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| L05-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 21-Oct-14 A | 14-Nov-14 A | |
| L08-8126 | Install Doors | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L10-8118 | Fire Alarm Trim | 2 | 0 | 21-Oct-14 A | 21-Oct-14 A | |

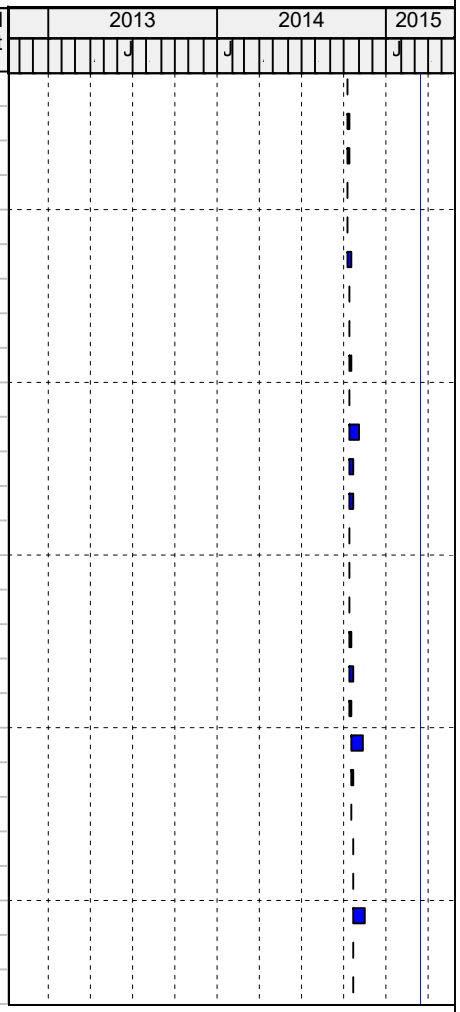



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8126 | Install Doors | 2 | 0 | 22-Oct-14 A | 23-Oct-14 A | |
| L11-8118 | Fire Alarm Trim | 2 | 0 | 22-Oct-14 A | 22-Oct-14 A | |
| L06-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 23-Oct-14 A | 19-Nov-14 A | |
| L10-8126 | Install Doors | 2 | 0 | 23-Oct-14 A | 27-Oct-14 A | |
| L12-8124 | Install Flooring | 5 | 0 | 23-Oct-14 A | 29-Oct-14 A | |
| L12-8118 | Fire Alarm Trim | 2 | 0 | 23-Oct-14 A | 23-Oct-14 A | |
| L11-8116 | Install Base and Door Thresholds | 5 | 0 | 24-Oct-14 A | 26-Nov-14 A | |
| L07-8110 | HVAC Grilles & Registers | 2 | 0 | 27-Oct-14 A | 28-Oct-14 A | |
| L10-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |
| L11-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |
| L17-8102 | Hang GWB & Inspection | 4 | 0 | 27-Oct-14 A | 03-Nov-14 A | |
| L07-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 28-Oct-14 A | 26-Nov-14 A | |
| L08-8120 | Bathrooms - Install Countertops | 3 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L11-8126 | Install Doors | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L12-8108 | Lighting and Electrical Trim | 3 | 0 | 28-Oct-14 A | 30-Oct-14 A | |
| L12-8116 | Install Base and Door Thresholds | 5 | 0 | 28-Oct-14 A | 03-Dec-14 A | |
| L14-8118 | Fire Alarm Trim | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L05-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Oct-14 A | 31-Oct-14 A | |
| L06-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Oct-14 A | 31-Oct-14 A | |
| L12-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L14-8108 | Lighting and Electrical Trim | 3 | 0 | 29-Oct-14 A | 03-Nov-14 A | |
| L14-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8118 | Fire Alarm Trim | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L04-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 30-Oct-14 A | 04-Nov-14 A | |
| L07-8120 | Bathrooms - Install Countertops | 3 | 0 | 03-Nov-14 A | 05-Nov-14 A | |
| L08-8110 | HVAC Grilles & Registers | 2 | 0 | 03-Nov-14 A | 04-Nov-14 A | |

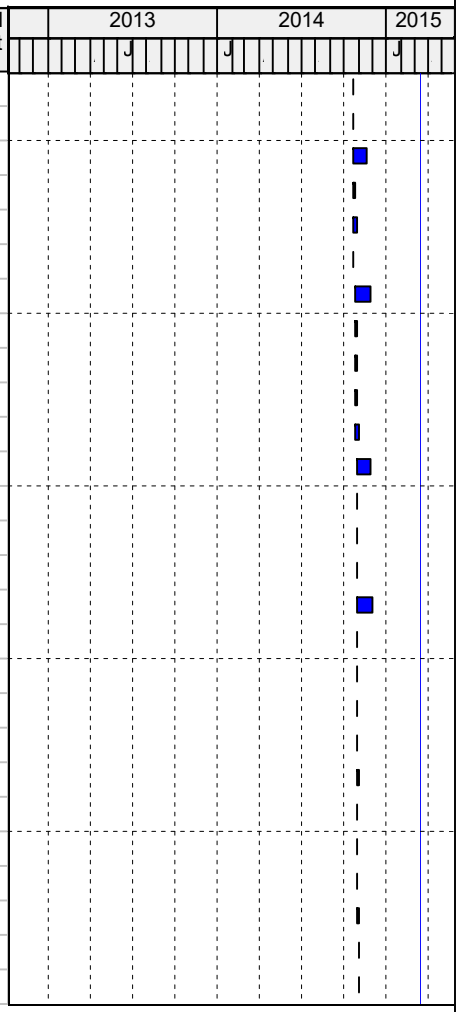



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8120 | Bathrooms - Install Countertops | 3 | 0 | 03-Nov-14 A | 05-Nov-14 A | |
| L10-8120 | Bathrooms - Install Countertops | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| L15-8108 | Lighting and Electrical Trim | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| L11-8120 | Bathrooms - Install Countertops | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| L16-8104 | Paint - Prime | 2 | 0 | 05-Nov-14 A | 06-Nov-14 A | |
| L05-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 07-Nov-14 A | 12-Nov-14 A | |
| L16-8105 | Paint - First Coat & Ceilings | 3 | 0 | 07-Nov-14 A | 11-Nov-14 A | |
| L12-8120 | Bathrooms - Install Countertops | 3 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L14-8124 | Install Flooring | 5 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L06-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 13-Nov-14 A | 17-Nov-14 A | |
| L15-8124 | Install Flooring | 5 | 0 | 17-Nov-14 A | 25-Nov-14 A | |
| L17-8104 | Paint - Prime | 2 | 0 | 17-Nov-14 A | 18-Nov-14 A | |
| L14-8116 | Install Base and Door Thresholds | 5 | 0 | 18-Nov-14 A | 08-Dec-14 A | |
| L16-8126 | Install Doors | 2 | 0 | 18-Nov-14 A | 19-Nov-14 A | |
| L07-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 19-Nov-14 A | 25-Nov-14 A | |
| L15-8116 | Install Base and Door Thresholds | 5 | 0 | 20-Nov-14 A | 08-Dec-14 A | |
| L03-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L04-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L05-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L08-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| L17-8105 | Paint - First Coat & Ceilings | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L16-8124 | Install Flooring | 5 | 0 | 25-Nov-14 A | 03-Dec-14 A | |
| L16-8112 | Fire Sprinkler Trim | 2 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| L16-8118 | Fire Alarm Trim | 2 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| L06-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L07-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L08-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 01-Dec-14 A | 08-Dec-14 A | |

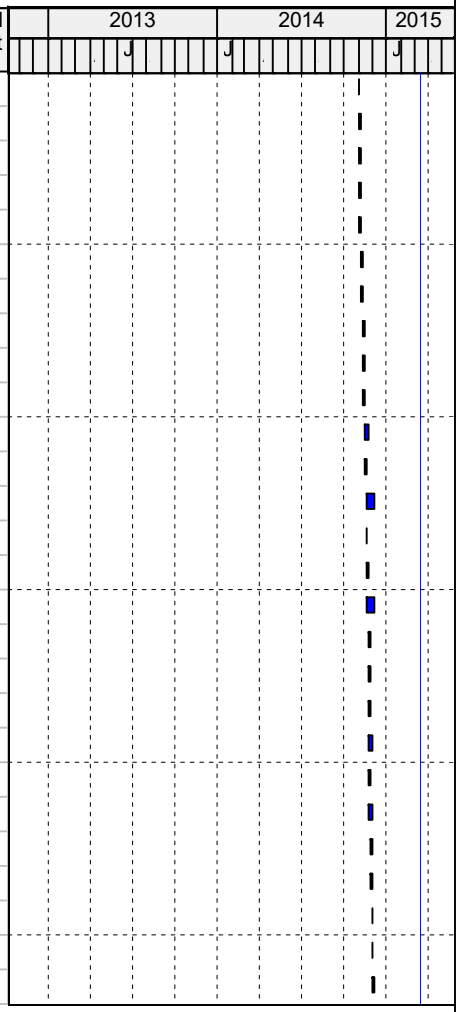


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L09-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 01-Dec-14 A | 10-Dec-14 A | |
| L16-8108 | Lighting and Electrical Trim | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L17-8126 | Install Doors | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| L16-8116 | Install Base and Door Thresholds | 5 | 0 | 02-Dec-14 A | 15-Dec-14 A | |
| L17-8112 | Fire Sprinkler Trim | 2 | 0 | 02-Dec-14 A | 02-Dec-14 A | |
| L09-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 03-Dec-14 A | 08-Dec-14 A | |
| L09-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L10-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L11-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L17-8118 | Fire Alarm Trim | 2 | 0 | 03-Dec-14 A | 03-Dec-14 A | |
| L12-8107 | Paint Final Coat | 3 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L14-8120 | Bathrooms - Install Countertops | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L17-8108 | Lighting and Electrical Trim | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L10-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L15-8120 | Bathrooms - Install Countertops | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 10-Dec-14 A | 16-Dec-14 A | |
| L11-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 10-Dec-14 A | 24-Dec-14 A | |
| L04-8132 | Contractor Punchlist (inspect/distribute/correct/back-pl | 7 | 0 | 11-Dec-14 A | 05-Feb-15 A | |
| L04-8134 | Final Clean @ Guestrooms | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L05-8132 | Contractor Punchlist (inspect/distribute/correct/back-pl | 7 | 0 | 12-Dec-14 A | 10-Feb-15 A | |
| L05-8134 | Final Clean @ Guestrooms | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L11-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 12-Dec-14 A | 17-Dec-14 A | |
| L06-8134 | Final Clean @ Guestrooms | 5 | 0 | 13-Dec-14 A | 13-Dec-14 A | |
| L12-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 15-Dec-14 A | 18-Dec-14 A | |
| L17-8124 | Install Flooring | 5 | 0 | 15-Dec-14 A | 18-Dec-14 A | |
| L17-8116 | Install Base and Door Thresholds | 5 | 0 | 18-Dec-14 A | 30-Dec-14 A | |

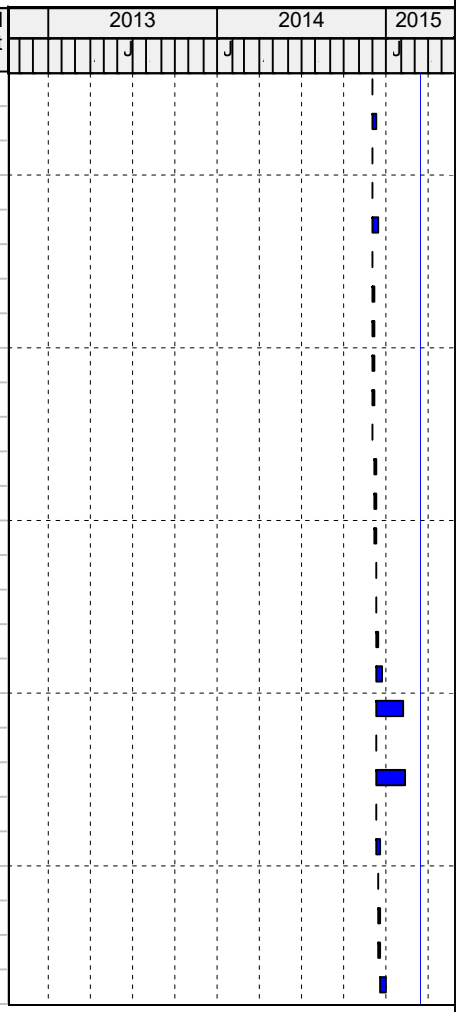



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| L14-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| L15-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 29-Dec-14 A | 05-Jan-15 A | |
| L16-8120 | Bathrooms - Install countertops | 3 | 0 | 29-Dec-14 A | 09-Jan-15 A | |
| L14-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 30-Dec-14 A | 05-Jan-15 A | |
| L15-8122 | Bathrooms - Plumbing fixtures & trim | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L16-8128 | Bathrooms - Install shower/tub surrounds | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L16-8122 | Bathrooms - Plumbing fixtures & trim | 3 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8128 | Bathrooms - Install shower/tub surrounds | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L09-8110 | HVAC grilles & registers | 2 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| L11-8110 | HVAC grilles & registers | 2 | 0 | 21-Jan-15 A | 28-Jan-15 A | |
| L12-8110 | HVAC grilles & registers | 2 | 0 | 21-Jan-15 A | 28-Jan-15 A | |
| L14-8110 | HVAC grilles & registers | 2 | 0 | 21-Jan-15 A | 02-Feb-15 A | |
| L10-8110 | HVAC grilles & registers | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L15-8110 | HVAC grilles & registers | 2 | 0 | 03-Feb-15 A | 16-Feb-15 A | |
| L16-8110 | HVAC grilles & registers | 2 | 0 | 03-Feb-15 A | 23-Feb-15 A | |
| L17-8122 | Bathrooms - Plumbing fixtures & trim | 3 | 2 | 03-Feb-15 A | 23-Mar-15 | 15 |
| L17-8120 | Bathrooms - Install countertops | 3 | 1 | 03-Feb-15 A | 18-Mar-15 | 15 |
| L06-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 04-Feb-15 A | 12-Feb-15 A | |
| L07-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 06-Feb-15 A | 20-Feb-15 A | |
| L14-8107 | Paint, final coat & touch-up | 3 | 0 | 09-Feb-15 A | 11-Feb-15 A | |
| L17-8110 | HVAC grilles & registers | 2 | 1 | 09-Feb-15 A | 20-Mar-15 | 16 |
| L08-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 10-Feb-15 A | 07-Mar-15 A | |
| L09-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 12-Feb-15 A | 06-Mar-15 A | |
| L15-8107 | Paint, final coat & touch-up | 3 | 0 | 16-Feb-15 A | 18-Feb-15 A | |
| L10-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 18-Feb-15 A | 13-Mar-15 A | |
| L11-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 2 | 20-Feb-15 A | 17-Mar-15 | 15 |

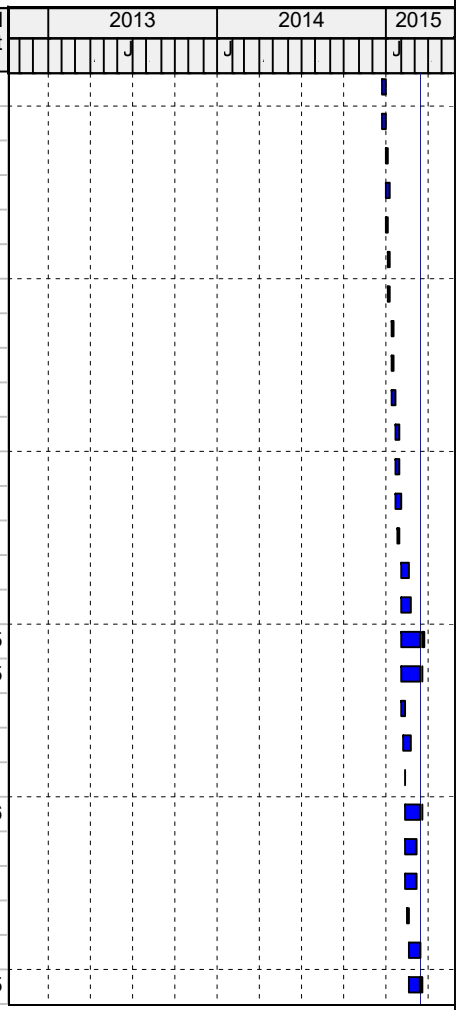


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8107 | Paint, final coat & touch-up | 3 | 0 | 24-Feb-15 A | 26-Feb-15 A | |
| L12-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 3 | 25-Feb-15 A | 18-Mar-15 | 15 |
| L14-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 5 | 26-Feb-15 A | 20-Mar-15 | 15 |
| L03-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L04-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L05-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L06-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L07-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L08-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L09-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L10-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L11-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L12-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L14-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L15-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L16-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L17-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L15-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 5 | 06-Mar-15 A | 25-Mar-15 | 15 |
| L16-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 7 | 10-Mar-15 A | 27-Mar-15 | 15 |
| L17-8107 | Paint, final coat & touch-up | 2 | 2 | 23-Mar-15 | 24-Mar-15 | 16 |
| L17-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 26-Mar-15 | 01-Apr-15 | 15 |
| L03-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 30-Mar-15 | 03-Apr-15 | 20 |
| **Pool Area** | | | | | | |
| L03-8216 | Install pool tile, coping and depth markers | 5 | 5 | 09-Apr-15 | 15-Apr-15 | 0 |
| **Corridors / Common / Public Areas** | | | | | | |
| L03-8200 | Vinyl Wall Coverings | 3 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L04-8200 | Vinyl Wall Coverings | 5 | 0 | 06-Aug-14 A | 12-Aug-14 A | |

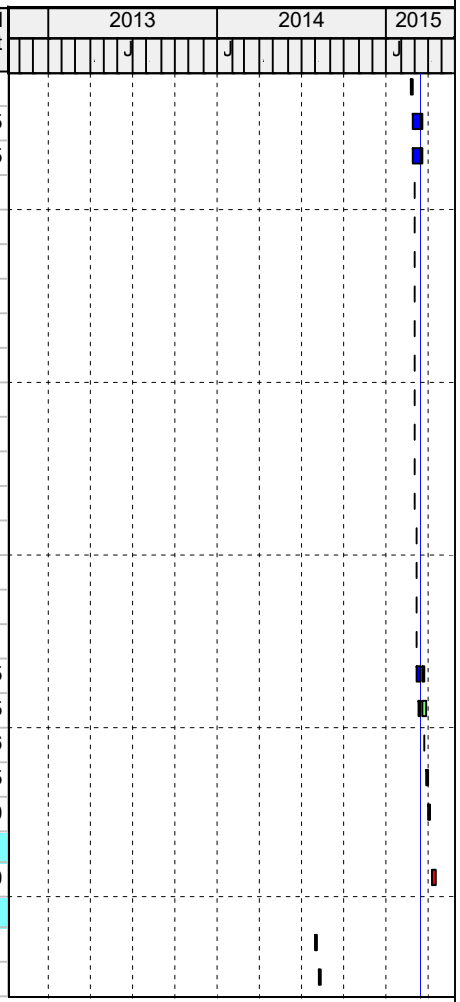


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8200 | Vinyl Wall Coverings | 5 | 0 | 12-Aug-14 A | 22-Sep-14 A | |
| L03-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L06-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L08-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 11-Sep-14 A | 19-Sep-14 A | |
| L04-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| L05-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L06-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L07-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L09-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| L10-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 08-Oct-14 A | |
| L11-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 10-Oct-14 A | |
| L08-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L12-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| L09-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L14-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 16-Oct-14 A | 27-Oct-14 A | |
| L10-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |
| L11-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L15-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 22-Oct-14 A | 29-Oct-14 A | |
| L12-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 03-Nov-14 A | 04-Nov-14 A | |
| L14-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L15-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 05-Nov-14 A | 06-Nov-14 A | |
| L16-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 14-Nov-14 A | 20-Nov-14 A | |
| L16-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L17-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L17-8200 | Wall coverings - vinyl at window niches & outside batl | 4 | 2 | 15-Dec-14 A | 17-Mar-15 | 15 |
| L04-8206 | Flooring - carpet at corridors | 2 | 0 | 14-Jan-15 A | 23-Jan-15 A | |

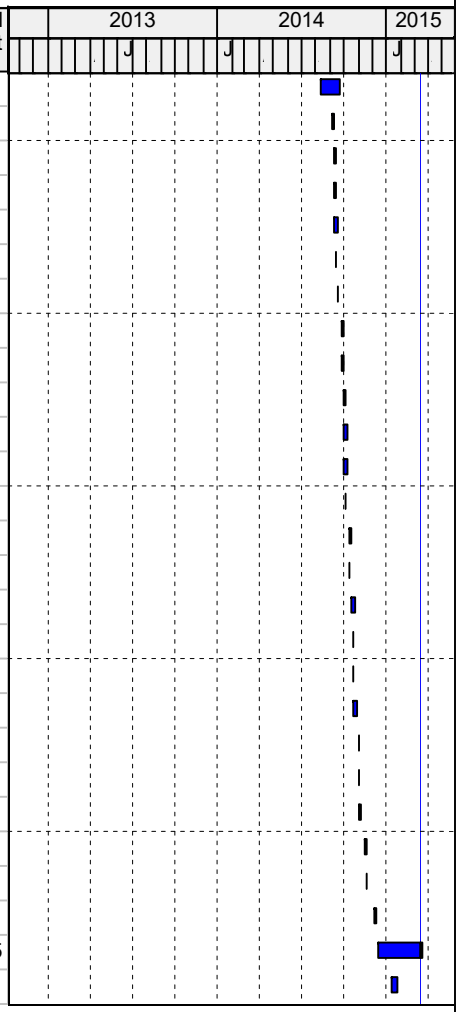


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8206 | Flooring - carpet at corridors | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| L07-8206 | Flooring - carpet at corridors | 2 | 0 | 22-Jan-15 A | 23-Jan-15 A | |
| L06-8206 | Flooring - carpet at corridors | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L09-8206 | Flooring - carpet at corridors | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| L08-8206 | Flooring - carpet at corridors | 2 | 0 | 04-Feb-15 A | 05-Feb-15 A | |
| L10-8206 | Flooring - carpet at corridors | 2 | 0 | 06-Feb-15 A | 09-Feb-15 A | |
| L11-8206 | Flooring - carpet at corridors | 2 | 0 | 10-Feb-15 A | 11-Feb-15 A | |
| L12-8206 | Flooring - carpet at corridors | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| L04-8208 | Final Cleaning | 2 | 0 | 13-Feb-15 A | 16-Feb-15 A | |
| L14-8206 | Flooring - carpet at corridors | 2 | 0 | 13-Feb-15 A | 14-Feb-15 A | |
| L15-8206 | Flooring - carpet at corridors | 2 | 0 | 16-Feb-15 A | 17-Feb-15 A | |
| L04-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 17-Feb-15 A | 03-Mar-15 A | |
| L05-8208 | Final Cleaning | 2 | 0 | 17-Feb-15 A | 18-Feb-15 A | |
| L05-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 18-Feb-15 A | 05-Mar-15 A | |
| L16-8206 | Flooring - carpet at corridors | 2 | 0 | 18-Feb-15 A | 19-Feb-15 A | |
| L06-8208 | Final Cleaning | 2 | 0 | 20-Feb-15 A | 25-Feb-15 A | |
| L03-8206 | Flooring - carpet at corridors (N-S leg) | 2 | 0 | 25-Feb-15 A | 25-Feb-15 A | |
| L06-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 4 | 0 | 25-Feb-15 A | 10-Mar-15 A | |
| L07-8208 | Final Cleaning | 2 | 0 | 27-Feb-15 A | 02-Mar-15 A | |
| L04-8214 | Floor Complete | 0 | 0 | | 03-Mar-15 A | |
| L07-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 1 | 05-Mar-15 A | 16-Mar-15 | 13 |
| L08-8208 | Final Cleaning | 2 | 0 | 05-Mar-15 A | 06-Mar-15 A | |
| L05-8214 | Floor Complete | 0 | 0 | | 05-Mar-15 A | |
| L08-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 1 | 06-Mar-15 A | 16-Mar-15 | 17 |
| L06-8214 | Floor Complete | 0 | 0 | | 10-Mar-15 A | |
| L09-8208 | Final Cleaning | 2 | 0 | 12-Mar-15 A | 13-Mar-15 A | |
| L09-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 4 | 12-Mar-15 A | 19-Mar-15 | 14 |

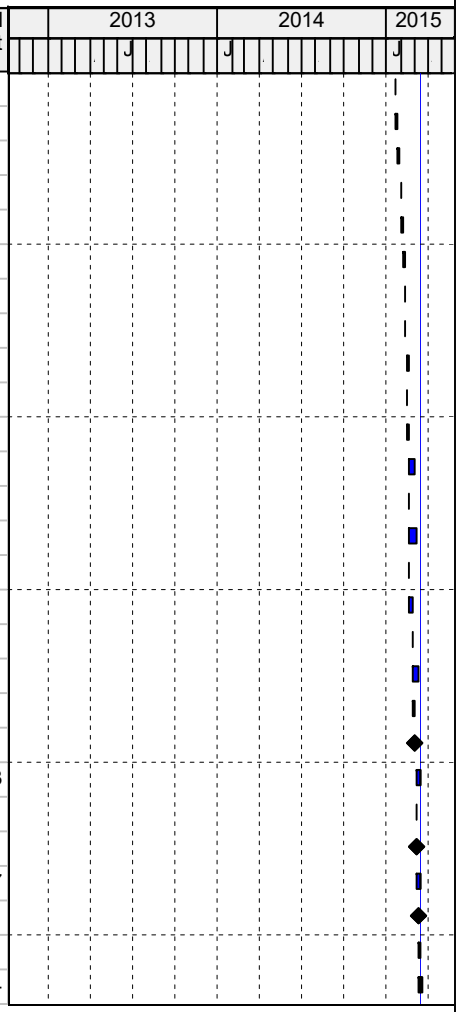



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8208 | Final Cleaning | 2 | 2 | 16-Mar-15 | 17-Mar-15 | 15 |
| L07-8214 | Floor Complete | 0 | 0 | | 16-Mar-15 | 13 |
| L08-8214 | Floor Complete | 0 | 0 | | 16-Mar-15 | 17 |
| L10-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 7 | 7 | 17-Mar-15 | 25-Mar-15 | 15 |
| L11-8208 | Final Cleaning | 2 | 2 | 17-Mar-15 | 18-Mar-15 | 15 |
| L11-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 6 | 6 | 18-Mar-15 | 25-Mar-15 | 15 |
| L12-8208 | Final Cleaning | 2 | 2 | 19-Mar-15 | 20-Mar-15 | 15 |
| L09-8214 | Floor Complete | 0 | 0 | | 19-Mar-15 | 14 |
| L12-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 8 | 8 | 23-Mar-15 | 01-Apr-15 | 15 |
| L14-8208 | Final Cleaning | 2 | 2 | 23-Mar-15 | 24-Mar-15 | 15 |
| L17-8206 | Flooring - carpet at corridors | 2 | 2 | 24-Mar-15 | 25-Mar-15 | 15 |
| L14-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 6 | 6 | 25-Mar-15 | 01-Apr-15 | 15 |
| L10-8214 | Floor Complete | 0 | 0 | | 25-Mar-15 | 15 |
| L11-8214 | Floor Complete | 0 | 0 | | 25-Mar-15 | 15 |
| L15-8208 | Final Cleaning | 2 | 2 | 26-Mar-15 | 27-Mar-15 | 15 |
| L15-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 8 | 8 | 30-Mar-15 | 08-Apr-15 | 15 |
| L16-8208 | Final Cleaning | 2 | 2 | 30-Mar-15 | 31-Mar-15 | 15 |
| L16-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 6 | 6 | 01-Apr-15 | 08-Apr-15 | 15 |
| L12-8214 | Floor Complete | 0 | 0 | | 01-Apr-15 | 15 |
| L14-8214 | Floor Complete | 0 | 0 | | 01-Apr-15 | 15 |
| L17-8208 | Final Cleaning | 2 | 2 | 02-Apr-15 | 03-Apr-15 | 15 |
| L17-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 7 | 7 | 03-Apr-15 | 13-Apr-15 | 15 |
| L03-8208 | Final Cleaning | 2 | 2 | 06-Apr-15 | 07-Apr-15 | 20 |
| L03-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 07-Apr-15 | 13-Apr-15 | 20 |
| L15-8214 | Floor Complete | 0 | 0 | | 08-Apr-15 | 15 |
| L16-8214 | Floor Complete | 0 | 0 | | 08-Apr-15 | 15 |
| L17-8214 | Floor Complete | 0 | 0 | | 13-Apr-15 | 15 |

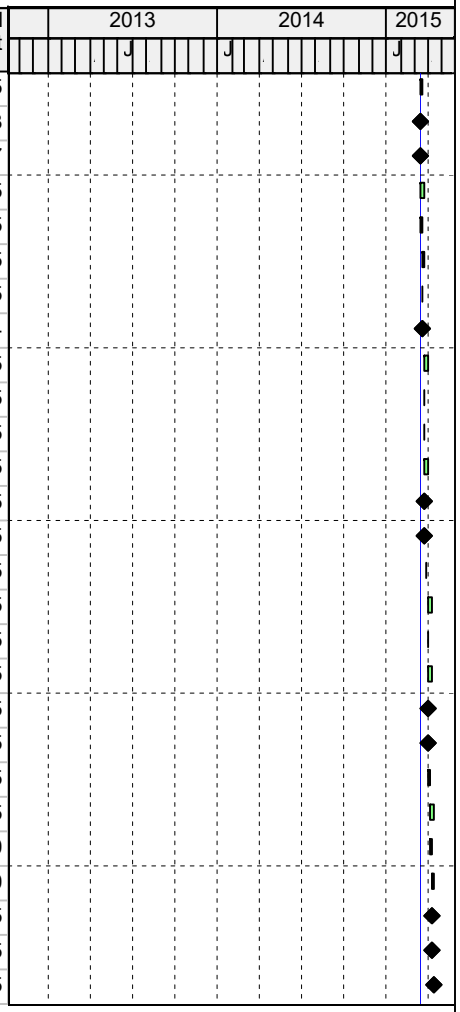


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8214 | Floor Complete | 0 | 0 | | 11-May-15 | 0 |
| **Mech Penthouse** | | | | | | |
| PH-8100 | PH - Insulation & Vapor Barrier | 5 | 0 | 09-Oct-14 A | 13-Oct-14 A | |
| PH-8102 | PH - Complete GWB Hang / Tape / Finish | 6 | 0 | 14-Oct-14 A | 10-Nov-14 A | |
| PH-8122 | PH - Plumbing Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8110 | PH - HVAC Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8126 | PH - install doors & hardware | 2 | 0 | 24-Nov-14 A | 23-Feb-15 A | |
| PH-8104 | PH - Int Painting [DELETED] | 4 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| PH-8108 | PH - Elec Trim / Finish | 5 | 0 | 01-Dec-14 A | 19-Jan-15 A | |
| PH-8114 | PH - Install Stairs to Roof [DELETED] | 1 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| PH-8118 | PH - Fire Alarm Trim (speaker/strobe & smoke detecto | 5 | 0 | 01-Dec-14 A | 21-Jan-15 A | |
| PH-8124 | PH - Flooring [DELETED, NIC] | 5 | 0 | 01-Jan-15 A | 01-Jan-15 A | |
| PH-8134 | PH - Final Trims and Touch-Up | 3 | 3 | 16-Mar-15 | 18-Mar-15 | 39 |
| PH-8132 | PH - Contractor Pre-Punchlist | 1 | 1 | 20-Apr-15 | 20-Apr-15 | 16 |
| PH-8208 | PH - Final Clean | 1 | 1 | 21-Apr-15 | 21-Apr-15 | 16 |
| PH-8212 | PH - Final Punchlist | 1 | 1 | 22-Apr-15 | 22-Apr-15 | 16 |
| PH-8214 | PH - Floor Complete | 0 | 0 | | 22-Apr-15 | 16 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| **Smoke Control** | | | | | | |
| CO-7104 | Fire Alarm/Smoke Control Pre-Functional Testing - Po | 10 | 10 | 28-Apr-15 | 11-May-15 | 0 |
| CO-7106 | City of Bellevue Smoke Control Functional Acceptanc | 5 | 5 | 12-May-15 | 18-May-15 | 0 |
| CO-7108 | Final Marriott Smoke Control Funcational Acceptance | 2 | 2 | 19-May-15 | 20-May-15 | 0 |
| **Fire Sprinklers** | | | | | | |
| CO-7114 | Marriott Fire Sprinkler Funcational Acceptance Testing | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7110 | Fire Sprinkler Pre-Testing (Podium) | 3 | 3 | 13-Apr-15 | 15-Apr-15 | 11 |
| CO-7112 | City of Bellevue Fire Sprinkler Final Inspection | 5 | 5 | 12-May-15 | 18-May-15 | 0 |

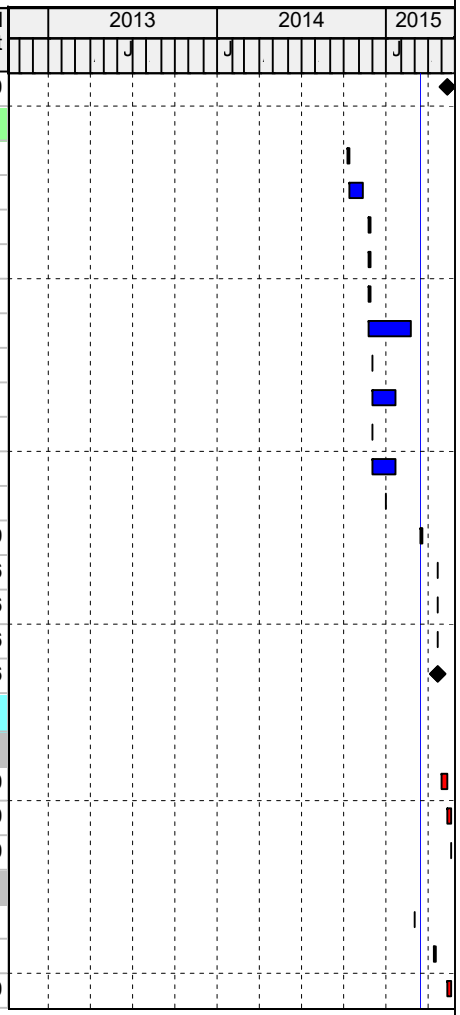


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Fire Alarm** | | | | | | |
| CO-7116 | Fire Alarm Pre-Testing (Podium) [DELETED] | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7118 | City of Bellevue Fire Alarm Functional Acceptance Tes | 5 | 5 | 12-May-15 | 18-May-15 | 0 |
| CO-7120 | Marriott Fire Alarm Funcational Acceptance Testing | 2 | 2 | 19-May-15 | 20-May-15 | 0 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| CO-7100 | Cx - Start-Up - Garage Exhaust Fan and VFD's | 4 | 4 | 23-Mar-15* | 26-Mar-15 | 32 |
| CO-7102 | Cx - DDC Point-To-Point - Garage Exhaust Fans | 5 | 5 | 27-Mar-15 | 02-Apr-15 | 32 |

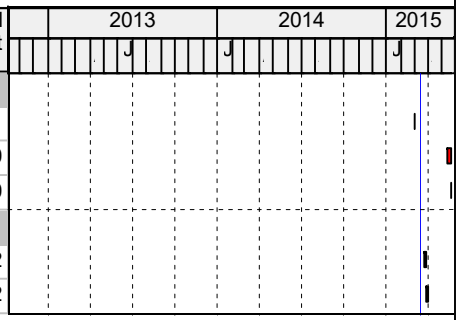



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Working Schedule - 4-13-15 Update** | | | | | | |
| I-4500 | Re-design building exterior (change from EIFS panels | 30 | 0 | 12-Apr-13 A | 28-May-14 A | |
| ASI01 | ASI No. 1 - Tower Crane Foundation Changes | 0 | 0 | 09-May-13 A | | |
| I-2292 | RFI 233/ Original HVAC submittal with specified damp | 1 | 0 | 13-May-13 A | 12-Jun-13 A | |
| ASI03 | ASI No. 3 - Food Service Plans and Cut Sheets | 0 | 0 | 14-May-13 A | | |
| ASI04 | ASI No. 4 - Revised Structural For The Podium | 0 | 0 | 22-May-13 A | | |
| ASI05 | ASI No. 5 - NTI Drawings | 0 | 0 | 22-May-13 A | | |
| I-1500 | Owner release revised LV design - Tower (ASIs 5, 13, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-1550 | Owner release revised LV design - Podium (ASIs 5, 1 | 200 | 0 | 23-May-13 A | 28-Apr-14 A | |
| I-1900 | Owner issue design revisions (ASIs 4, 9, 19, 34) | 215 | 0 | 23-May-13 A | 24-Mar-14 A | |
| I-2500 | Owner issue LL1 electrical revisions (ASIs 7, 9r2, 14, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| ASI02 | ASI No. 2 - Foundation Drainage System | 0 | 0 | 05-Jun-13 A | | |
| ASI04c | ASI No. 4 - Revised Structural For The Podium (Clouc | 0 | 0 | 05-Jun-13 A | | |
| ASI07 | ASI No. 7 - Electrical Rev-10 Changes | 0 | 0 | 18-Jun-13 A | | |
| ASI06 | ASI No. 6 - Mechanical Rev-8 Changes | 0 | 0 | 19-Jun-13 A | | |
| I-3700 | Owner resolve wall condition between stair and Eleva | 200 | 0 | 27-Jun-13 A | 16-Jun-14 A | |
| MM-1000 | MM - Temporary Power Available | 0 | 0 | 08-Jul-13 A | | |
| I-2100 | Owner revise roof steel design (Submittals 365, 370, | 200 | 0 | 09-Jul-13 A | 07-Apr-14 A | |
| I-2200 | Owner resolve elevator steel issue (RFI 112, RFI 112. | 200 | 0 | 09-Jul-13 A | 03-Mar-14 A | |
| I-2400 | Owner provide Tower light fixture selections (ASI 36) | 185 | 0 | 18-Jul-13 A | 08-Apr-14 A | |
| I-3400 | Owner provide Level 2 ceiling heights (RFI 465) | 180 | 0 | 19-Jul-13 A | 01-Jul-14 A | |
| I-2294 | RFI 233/ Revised HVAC submittal | 1 | 0 | 22-Jul-13 A | 25-Jul-13 A | |
| ASI04ca | ASI No. 4 - Revised Structural For The Podium (City A | 0 | 0 | 05-Aug-13 A | | |
| ASI11 | ASI No. 11 - Food and Beverage Drawing Revisions | 0 | 0 | 05-Aug-13 A | | |
| I-2900 | Owner revise Food Service and Kitchen (ASIs 11, 12, | 140 | 0 | 08-Aug-13 A | 27-Feb-14 A | |
| ASI12 | ASI No. 12 - Food and Beverage Drawing Changes | 0 | 0 | 12-Aug-13 A | | |
| ASI08 | ASI No. 8 - Provent System | 0 | 0 | 15-Aug-13 A | | |

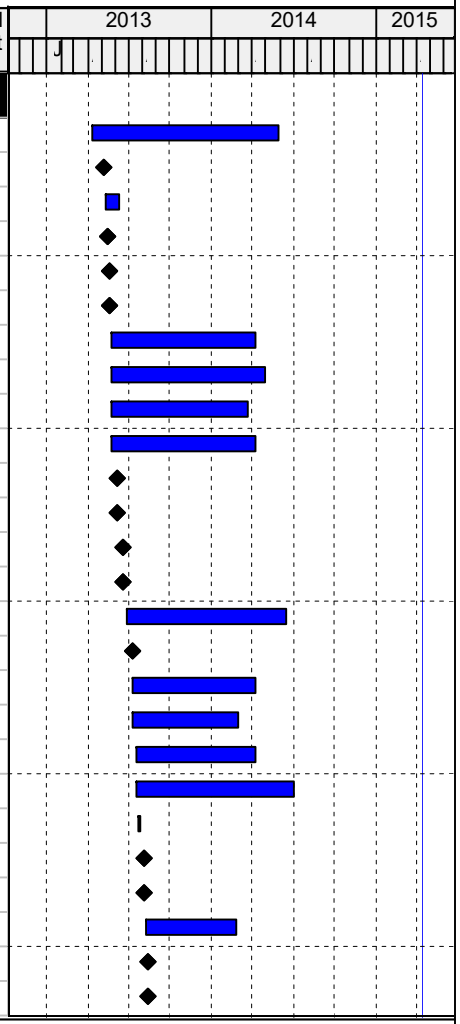


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| High Rise Hotel Sample Project | All Activities | Schedule Status Date 13-Apr-15 |
|---|---|---|

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-5010 | RFI 173 - Porte Cochere Bench Design | 1 | 0 | 16-Aug-13 A | 04-Sep-13 A | |
| I-5012 | RFI 189 - Porte Cochere Pavement Design | 1 | 0 | 26-Aug-13 A | 30-Jun-14 A | |
| I-1400 | Owner develop envelope redesign | 70 | 0 | 27-Aug-13 A | 12-Dec-13 A | |
| I-5014 | RFI 197 - LL1 & LL2 Planter Drain Pipes | 1 | 0 | 03-Sep-13 A | 06-Sep-13 A | |
| I-3600 | Owner closeout glass/glazing allowance | 160 | 0 | 04-Sep-13 A | 30-Apr-14 A | |
| ASI09 | ASI No. 9 - Incorporating Arch, MEP & Struct Drawing | 0 | 0 | 05-Sep-13 A | | |
| I-1200 | Owner release revised Concierge Lounge design (AS | 160 | 0 | 06-Sep-13 A | 22-Oct-14 A | |
| ASI13 | ASI No. 13 - NTI Drawing Updates | 0 | 0 | 06-Sep-13 A | | |
| I-2800 | Owner revise interior public space design (ASIs 16, 1 | 130 | 0 | 25-Sep-13 A | 09-Apr-14 A | |
| ASI16 | ASI No. 16 - 9.20..13 General ID Releasae | 0 | 0 | 25-Sep-13 A | | |
| I-2296 | RFI 233/ Issue RFI and receive response | 1 | 0 | 25-Sep-13 A | 21-Jan-14 A | |
| I-2000 | Owner approve door frames (Submittals 258, 454, 48 | 85 | 0 | 27-Sep-13 A | 23-Jan-14 A | |
| ASI14 | ASI No. 14 - Electrical Revisions for Low Voltage | 0 | 0 | 04-Oct-13 A | | |
| ASI17 | ASI No. 17 - Smoke Control Design 42C Permit | 0 | 0 | 09-Oct-13 A | | |
| ASI18 | ASI No. 18 - Interior Package Revisions | 0 | 0 | 15-Oct-13 A | | |
| I-3100 | Owner revise ballroom ceiling design (ASIs 18, 25) | 100 | 0 | 17-Oct-13 A | 25-Feb-14 A | |
| I-1600 | Owner provide directive for south & east corridor encl | 110 | 0 | 28-Oct-13 A | 18-Apr-14 A | |
| I-5016 | RFI 282 - Porte Cochere Planter Dimensions | 1 | 0 | 01-Nov-13 A | 21-Jan-14 A | |
| ASI11-12 | ASI No. 11 & 12 - Kitchen Equipment Specifications | 0 | 0 | 06-Nov-13 A | | |
| ASI09r1s | ASI No. 9 (Revised) - City Approved ASI No. 9 (Struct | 0 | 0 | 07-Nov-13 A | | |
| I-2600 | Owner resolve L2 slab coordination issue | 4 | 0 | 13-Nov-13 A | 16-Nov-13 A | |
| ASI09r1m | ASI No. 9 (Revised) - City Approved ASI No. 9 (Mecha | 0 | 0 | 15-Nov-13 A | | |
| ASI06r1 | ASI No. 6 (Revised) - Mechanical Rev-8 Changes (Cit | 0 | 0 | 19-Nov-13 A | | |
| ASI21 | ASI No. 21 - Revised Structural Drawings for the Roof | 0 | 0 | 22-Nov-13 A | | |
| I-2700 | Owner revise tower guest rooms design (ASIs 23, 29) | 58 | 0 | 04-Dec-13 A | 26-Feb-14 A | |
| ASI09r1e | ASI No. 9 (Revised) - ASI No. 9 Electrical Drawings (R | 0 | 0 | 04-Dec-13 A | | |
| ASI20 | ASI No. 20 - Dry Utilities Revisions | 0 | 0 | 05-Dec-13 A | | |

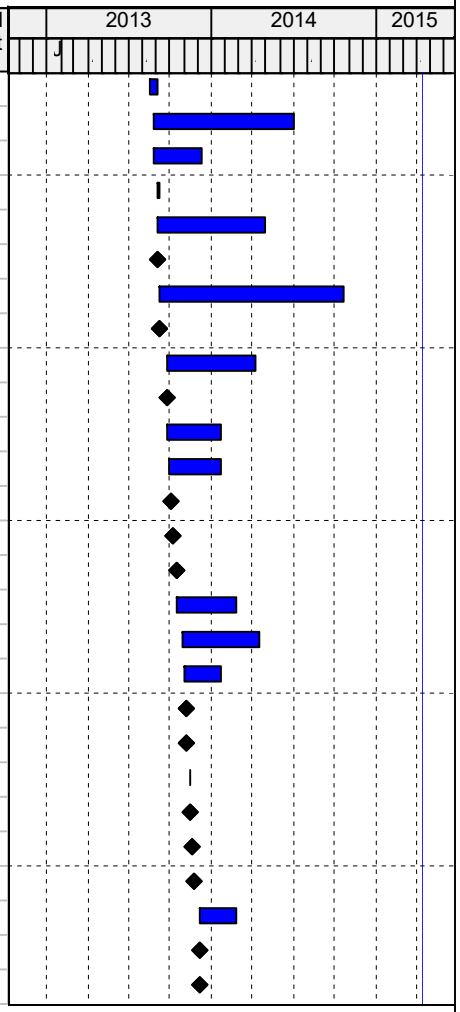


Actual Work
Remaining Work
Critical Remai...
Milestone



TASK filter: All Activities

© Oracle Corporation

| High Rise Hotel Sample Project | All Activities | Schedule Status Date 13-Apr-15 |
|---|---|---|

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1700 | Owner provide design for dry site utilities (ASIs 20, 20 | 66 | 0 | 09-Dec-13 A | 13-Mar-14 A | |
| I-1402 | Begin exterior panel production | 41 | 0 | 13-Dec-13 A | 12-Feb-14 A | |
| ASI17ca | ASI No. 17 - Smoke Control Design 42C Permit (City / | 0 | 0 | 16-Dec-13 A | | |
| ASI09r2e | ASI No. 9 (Revised) - ASI No. 9 Electrical Drawings (R | 0 | 0 | 18-Dec-13 A | | |
| I-1300 | Owner issue "Hold" directive (email) | 0 | 0 | | 19-Dec-13 A | |
| ASI22 | ASI No. 22 - Revised Door Schedule and Door Hardw | 0 | 0 | 19-Dec-13 A | | |
| I-1100 | Owner release revised L17 design (ASI 23, 29R1) | 74 | 0 | 20-Dec-13 A | 08-Apr-14 A | |
| I-1302 | Owner issue ASI 30 (Prep Kitchen Revisions) | 47 | 0 | 20-Dec-13 A | 27-Feb-14 A | |
| ASI23 | ASI No. 23 - Revised Tower and Enlarged Guestroom | 0 | 0 | 20-Dec-13 A | | |
| I-1404 | City of Bellevue Approval | 90 | 0 | 23-Dec-13 A | 15-Jul-14 A | |
| I-5470 | Resolve ceiling height issue at Laundy Room (RFI __ | 5 | 0 | 05-Jan-14 A | 30-Jan-15 A | |
| ASI15 | ASI No. 15 - NTI DV Drawings Revisions | 0 | 0 | 08-Jan-14 A | | |
| ASI09R2e2 | ASI No. 9 (Revised) - City Approved ASI No. 9 (Electri | 0 | 0 | 14-Jan-14 A | | |
| ASI22r1 | ASI No. 22 (Revised) - Architectural Revisions to Door | 0 | 0 | 20-Jan-14 A | | |
| I-3000 | ASI 38/ Owner revise bar area (change to straight bar | 71 | 0 | 22-Jan-14 A | 27-May-14 A | |
| I-2298 | RFI 233/ Resolve issue with designer & City | 1 | 0 | 22-Jan-14 A | 14-Mar-14 A | |
| ASI20r1 | ASI No. 20 (Revised) - Dry Utilities Revsions | 0 | 0 | 23-Jan-14 A | | |
| ASI24 | ASI No. 24 - FRCH ID Finish Schedule | 0 | 0 | 30-Jan-14 A | | |
| ASI26 | ASI No. 26 - Revised Laundry Layout and Equipment | 0 | 0 | 12-Feb-14 A | | |
| I-1306 | Prep Kitchen - Additional plumbing (ASI 30) | 4 | 0 | 17-Feb-14 A | 01-Aug-14 A | |
| ASI28 | ASI No. 28 - Guest Laundry Equipment Sheets | 0 | 0 | 20-Feb-14 A | | |
| ASI27 | ASI No. 27 - Mechanical, Electrical and Plumbing She | 0 | 0 | 21-Feb-14 A | | |
| ASI25 | ASI No. 25 - Podium Level Revisions (Stair 1 & 2 Gat | 0 | 0 | 24-Feb-14 A | | |
| ASI29 | ASI No. 29 - Architectural Tower and Guestroom Revis | 0 | 0 | 26-Feb-14 A | | |
| ASI30 | ASI No. 30 - Food Service Revisions per HEI | 0 | 0 | 27-Feb-14 A | | |
| I-2202 | Fabricate revised elevator steel | 60 | 0 | 04-Mar-14 A | 07-May-14 A | |
| I-2704 | Framing "Go Back" work for ASIs 23, 29 - L4 | 1 | 0 | 05-Mar-14 A | 12-Mar-14 A | |

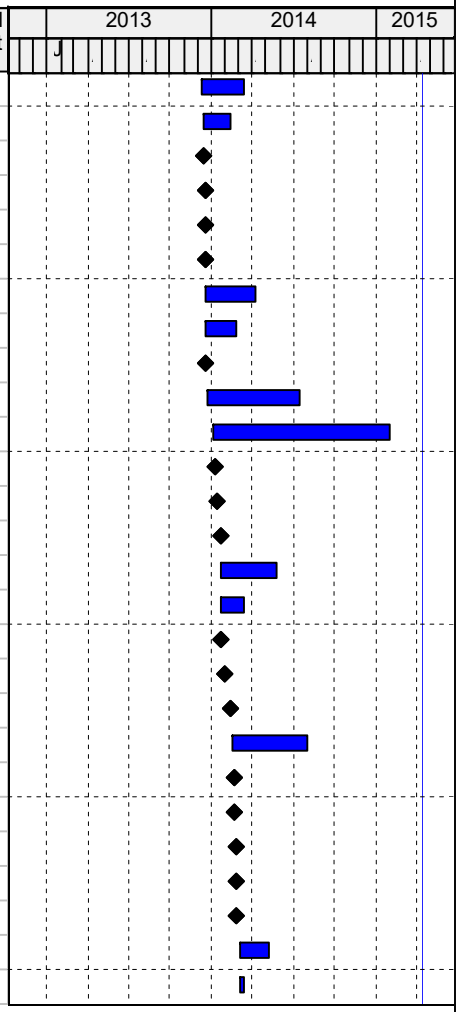


Actual Work | Critical Remai...
Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ASI31 | ASI No. 31 - Revised Elevations | 0 | 0 | 07-Mar-14 A | | |
| ASI33 | ASI No. 33 - NTI DV Drawing Revisions | 0 | 0 | 11-Mar-14 A | | |
| ASI20r2 | ASI No. 20 (Revised) - Dry Utilities Revisions | 0 | 0 | 13-Mar-14 A | | |
| I-1702 | Owner provide directive to proceed | 26 | 0 | 14-Mar-14 A | 01-May-14 A | |
| I-2300 | RFI 233/ Procure dampers | 1 | 0 | 15-Mar-14 A | 11-Apr-14 A | |
| I-3300 | Owner provide Guest Room plumbing fixture selectio | 1 | 0 | 20-Mar-14 A | 20-Mar-14 A | |
| ASI34 | ASI No. 34 - SCA Structural Revisions S6.01 and S6.( | 0 | 0 | 24-Mar-14 A | | |
| I-4600 | RFI 72, HHP3-HHP5 - resolve electrical issue & revise | 1 | 0 | 24-Mar-14 A | 09-Apr-14 A | |
| I-1902 | Procure revised structural steel | 15 | 0 | 25-Mar-14 A | 14-Apr-14 A | |
| I-3900 | Ballroom Parapet Height Issue/ RFI 471 | 1 | 0 | 28-Mar-14 A | 07-May-14 A | |
| I-3016 | ASI 38/ Scan Level 1 slab at bar (3 times) | 1 | 0 | 31-Mar-14 A | 11-Apr-14 A | |
| I-4000 | Owner complete design of east stitched enclosure (fo | 1 | 0 | 01-Apr-14 A | 14-May-14 A | |
| ASI35 | ASI No. 35 - FRCH ID Revisions and Finish Schedule | 0 | 0 | 07-Apr-14 A | | |
| I-2102 | Fabricate revised roof steel | 20 | 0 | 08-Apr-14 A | 15-May-14 A | |
| I-3200 | Owner provide light fixture selections for podium level | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| ASI36 | ASI No. 36 - MDP Electrical Revisions Rev. 16 | 0 | 0 | 08-Apr-14 A | | |
| ASI29r1 | ASI No. 29 (Revised) - Guestroom, Interior Elevation, | 0 | 0 | 09-Apr-14 A | | |
| I-3800 | Resolve  Heat Pump Electrical Overcurrent Issue | 20 | 0 | 23-Apr-14 A | 18-Jun-14 A | |
| L10-8221 | HVAC Risers Duct Insulation | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L11-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| ASI37 | ASI No. 37 - NTI DV Drawing Revisions | 0 | 0 | 28-Apr-14 A | | |
| I-2304 | RFI 233/ Framing "Go Back" work at L3 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2306 | RFI 233/ Framing "Go Back" work at L4 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2308 | RFI 233/ Framing "Go Back" work at L5 | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2706 | Framing "Go Back" work for ASIs 23, 29 - L5 | 1 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2708 | Framing "Go Back" work for ASIs 23, 29 - L6 | 1 | 0 | 29-Apr-14 A | 09-May-14 A | |

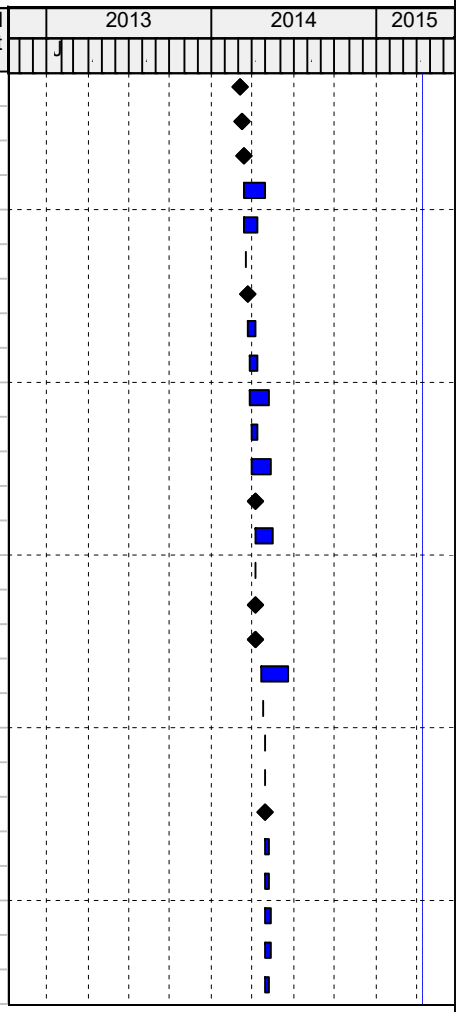



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-2702 | Framing "Go Back" work for ASIs 23, 29 - L3 | 1 | 0 | 01-May-14 A | 01-May-14 A | |
| I-1706 | PSE scheduling delay | 10 | 0 | 01-May-14 A | 20-May-14 A | |
| I-3602 | Complete shop drawings & fab/deliver storefront fram | 40 | 0 | 01-May-14 A | 14-Jun-14 A | |
| L04-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| I-3904 | Ballroom Parapet Height Issue/ re-engineer parapet | 1 | 0 | 06-May-14 A | 01-Jul-14 A | |
| I-1802 | Rework framing for door hold-opens - LL4 | 1 | 0 | 07-May-14 A | 08-May-14 A | |
| L04-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-May-14 A | 12-May-14 A | |
| ASI25r1 | ASI No. 25 (Revised) - Architectural Podium Level Re | 0 | 0 | 07-May-14 A | | |
| ASI29r2 | ASI No. 29 (Revised) - Architectural Tower and Guestı | 0 | 0 | 07-May-14 A | | |
| I-1800 | Owner issue directive to proceed with door hold-open | 1 | 0 | 08-May-14 A | 08-May-14 A | |
| I-1804 | Rework framing for door hold-opens - LL3 | 1 | 0 | 08-May-14 A | 09-May-14 A | |
| I-2312 | RFI 233/ Framing "Go Back" work at L7 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-2314 | RFI 233/ Framing "Go Back" work at L8 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-3902 | Install Ballroom parapet extension | 5 | 0 | 08-May-14 A | 13-May-14 A | |
| I-1806 | Rework framing for door hold-opens - LL2 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-1808 | Rework framing for door hold-opens - LL1 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-2310 | RFI 233/ Framing "Go Back" work at L6 | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| I-2710 | Framing "Go Back" work for ASIs 23, 29 - L7 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| L05-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L06-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L05-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| LL2E-8110 | LL2 - Electrical, Fire pumps/equipment final connectic | 5 | 0 | 12-May-14 A | 30-Oct-14 A | |
| I-2316 | RFI 233/ Install dampers | 1 | 0 | 12-May-14 A | 15-May-14 A | |
| PH-8704 | PH - Install Machine Support Steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| PH-8710 | Install elevator rail support steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| L03-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 13-May-14 A | 14-May-14 A | |

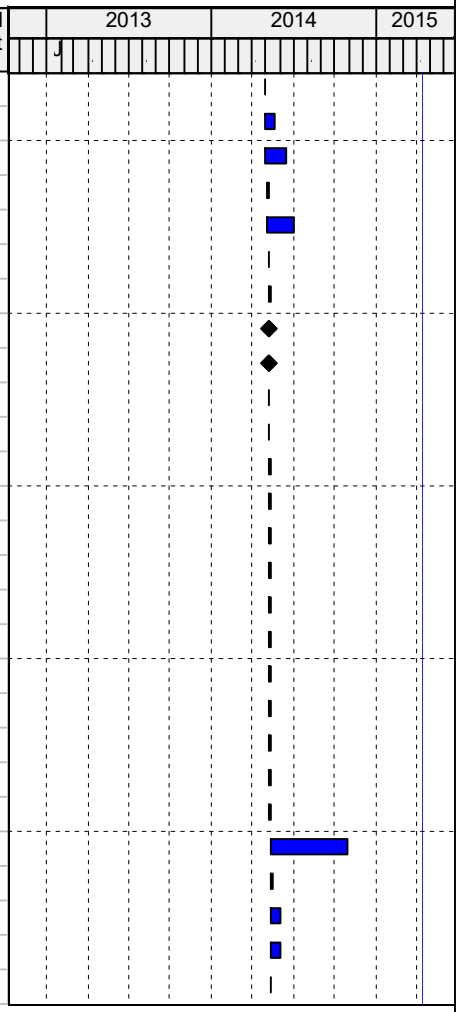



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 13-May-14 A | 14-May-14 A | |
| I-2318 | RFI 233/ Install dampers | 1 | 0 | 15-May-14 A | 19-May-14 A | |
| I-4002 | East Stitched - Install framing and windows | 9 | 0 | 19-May-14 A | 09-Jun-14 A | |
| I-2320 | RFI 233/ Install dampers | 1 | 0 | 20-May-14 A | 26-May-14 A | |
| L10-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L11-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L12-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| RF-4038 | AR - Concrete pads and curbs | 5 | 0 | 21-May-14 A | 04-Jun-14 A | |
| ASI27cap | ASI No. 27 - City Approved ASI No. 27 (Plumbing) | 0 | 0 | 21-May-14 A | | |
| ASI38 | ASI No. 38 - MDP's Bar & Concierge Plumbing Revisi | 0 | 0 | 22-May-14 A | | |
| L10-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L11-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L12-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L14-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L15-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 27-May-14 A | |
| L11-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 07-Jun-14 A | |
| L12-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 27-May-14 A | 06-Jun-14 A | |
| I-2322 | New Activity | 1 | 0 | 27-May-14 A | 28-May-14 A | |
| I-3002 | ASI 38/ City of Bellevue approve bar design changes | 5 | 0 | 28-May-14 A | 12-Dec-14 A | |
| I-4502 | Release metal panels for fabrication | 0 | 0 | 28-May-14 A | | |
| I-4504 | Metal panel fabrication (1st delivery) | 1 | 0 | 29-May-14 A | 08-Jul-14 A | |
| I-2324 | RFI 233/ Install dampers | 1 | 0 | 29-May-14 A | 08-Jun-14 A | |
| L16-8221 | HVAC Risers Duct Insulation | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| PH-8712 | PH - Complete Framing and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |

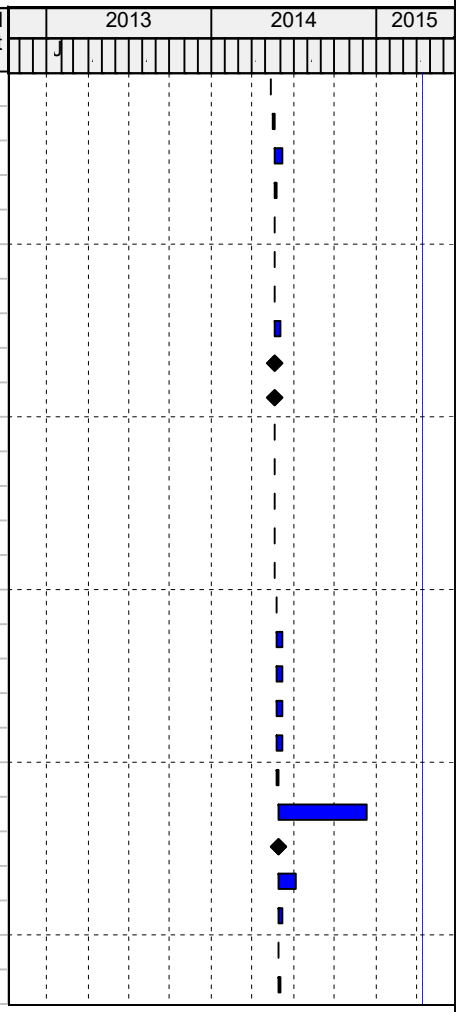



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-8714 | Stage PH/L18 roofing materials | 2 | 0 | 30-May-14 A | 30-May-14 A | |
| L08-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L08-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 02-Jun-14 A | 20-Jun-14 A | |
| PH-8704I | Correct support steel embeds | 2 | 0 | 02-Jun-14 A | 11-Jun-14 A | |
| L14-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 03-Jun-14 A | 04-Jun-14 A | |
| L17-8221 | HVAC Risers Duct Insulation | 1 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| PC-4010 | PC - Fireproof Entry Roof Steel | 5 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| I-4100 | Owner resolve trap primers issue (RFI 560) | 5 | 0 | 03-Jun-14 A | 20-Jun-14 A | |
| RF-6028 | Tower Roof - Structural Steel | 5 | 0 | 04-Jun-14 A | 17-Jun-14 A | |
| L14-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L1B-6005 | Head of Wall Fire Caulk at CMU (including East Servic | 2 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| ASI36r1 | ASI No. 36 (Revised) - MDP's Revision to E002 | 0 | 0 | 05-Jun-14 A | | |
| L14-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L15-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L16-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| ASI39 | ASI No. 39 - MDP's Electrical Revisions Rev. 17 | 0 | 0 | 09-Jun-14 A | | |
| I-2326 | RFI 233/ Install dampers | 1 | 0 | 09-Jun-14 A | 09-Jun-14 A | |
| I-2328 | RFI 233/ Install dampers | 1 | 0 | 09-Jun-14 A | 09-Jun-14 A | |
| I-2330 | RFI 233/ Install dampers | 1 | 0 | 10-Jun-14 A | 10-Jun-14 A | |
| L09-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 11-Jun-14 A | 12-Jun-14 A | |
| ASI25r2 | ASI No. 25 (Revised) - JBA's Interior Elevation Revisic | 0 | 0 | 11-Jun-14 A | | |
| ASI29r3 | ASI No. 29 (Revised) - JBA's Interior Elevation Revs a | 0 | 0 | 11-Jun-14 A | | |
| ASI35r1 | ASI No. 35 (Revised) - JBA's Interior Design Revisions | 0 | 0 | 11-Jun-14 A | | |

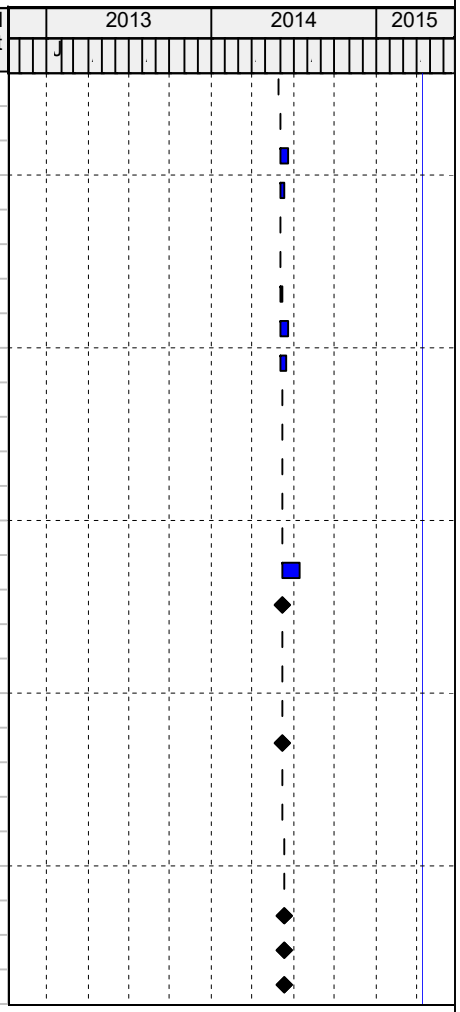


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-2332 | RFI 233/ Install dampers | 1 | 0 | 11-Jun-14 A | 12-Jun-14 A | |
| I-5018 | RFI 566 - Street Overlay Pavement Marking Reqs | 1 | 0 | 11-Jun-14 A | 01-Jul-14 A | |
| I-2970 | RFI 567 Grease Duct Conflict with Mens Restroom (P | 1 | 0 | 12-Jun-14 A | 01-Aug-14 A | |
| I-2336 | RFI 233/ Install dampers | 1 | 0 | 13-Jun-14 A | 16-Jun-14 A | |
| I-2334 | RFI 233/ Install dampers | 1 | 0 | 17-Jun-14 A | 18-Jun-14 A | |
| I-3702 | Complete wall framing at Stair/Elevator 5 (LL4) | 2 | 0 | 18-Jun-14 A | 20-Jun-14 A | |
| I-3720 | Fireproof added steel between Stair 1 and Elevator 5 | 5 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| I-3722 | Complete GWB between Stair 1 and Elevator 5 shaft | 10 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| ASI40 | ASI No. 40 - MDP's Electrical Revisions Rev. 18 | 0 | 0 | 18-Jun-14 A | | |
| LL1-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 22-Jul-14 A | |
| TC-5912 | Tower Crane pour-backs (LL4 to L3) | 4 | 0 | 19-Jun-14 A | 26-Jun-14 A | |
| LL1-Z2-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| I-2338 | RFI 233/ Install dampers | 1 | 0 | 19-Jun-14 A | 23-Jun-14 A | |
| LL4-6005 | LL4 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| LL3-6005 | LL3 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| L03-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 21-Jun-14 A | 21-Jun-14 A | |
| L06-6040 | Test Heat Pumps - L3, L4, L5 and L6 | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L03-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| L17-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL2-6005 | LL2 - Seismic Head Of Wall Fire Caulk at CMU | 5 | 0 | 24-Jun-14 A | 18-Jul-14 A | |
| I-3704 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL1-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z2-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z3-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 04-Aug-14 A | |
| L1L-6005 | Head of Wall Fire Caulk at CMU (including back of ho | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1K-6005 | Head of Wall Fire Caulk at CMU & Inspection | 2 | 0 | 24-Jun-14 A | 08-Aug-14 A | |
| L03-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |

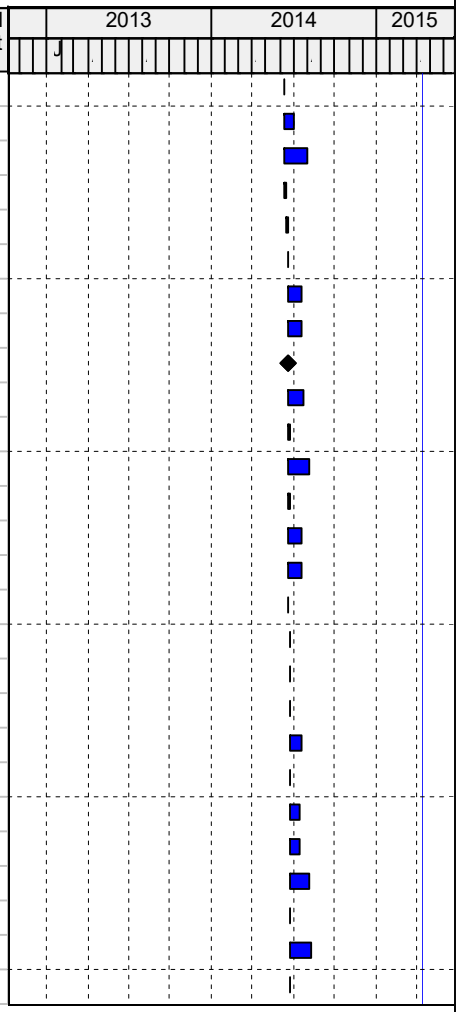



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| I-2340 | RFI 233/ Install dampers | 1 | 0 | 24-Jun-14 A | 26-Jun-14 A | |
| L17-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| I-3710 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| I-3712 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| L1K-6018a | Install Kitchen hoods and grease ducts (OFCI) | 10 | 0 | 25-Jun-14 A | 07-Oct-14 A | |
| L03-8604 | L3 Pool - Plumbing R/I | 5 | 0 | 25-Jun-14 A | 10-Nov-14 A | |
| ASI41 | ASI No. 41 - Kay Lang's Interior Design CD Set | 0 | 0 | 25-Jun-14 A | | |
| L04-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 26-Jun-14 A | 03-Jul-14 A | |
| L09-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 26-Jun-14 A | 26-Jun-14 A | |
| I-3706 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 26-Jun-14 A | 10-Jul-14 A | |
| L03-8600 | L3 Pool - Framing & HM frames | 5 | 0 | 26-Jun-14 A | 20-Nov-14 A | |
| L05-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L08-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L04-7018 | Electrical Rough-In | 1 | 0 | 27-Jun-14 A | 22-Jul-14 A | |
| L04-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 27-Jun-14 A | 23-Jul-14 A | |
| I-2342 | RFI 233/ Install dampers | 1 | 0 | 27-Jun-14 A | 28-Jun-14 A | |
| L03-7020 | HVAC Rough-In | 1 | 0 | 29-Jun-14 A | 15-Jul-14 A | |
| L1RR-8100 | Insulation [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8100 | Insulation [DELETED - included in Ballroom activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8100 | Insulation [DELETED - included in Meeting Rooms ac | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8102 | GWB Hang [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8215 | GWB Tape [DELETED - included in Meeting Rooms a | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8104 | Prime Paint [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |

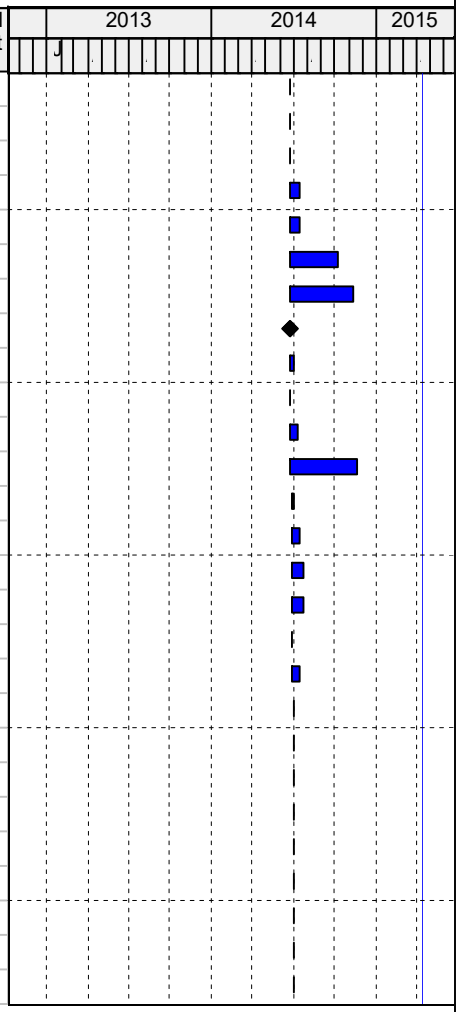



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z6-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8102 | GWB Hang [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8215 | GWB Tape [DELETED - included in Ballroom activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8104 | Prime Paint [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8102 | GWB Hang [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8215 | GWB Tape [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8104 | Prime Paint [DELETED - included in Kitchen activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L03-7018 | Electrical Rough-In | 1 | 0 | 01-Jul-14 A | 14-Jul-14 A | |
| L03-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Jul-14 A | 15-Jul-14 A | |
| I-5020 | RFI 583 - Tree Grate Location | 1 | 0 | 01-Jul-14 A | 23-Jul-14 A | |
| I-5022 | RFI 585 - Porte Cochere Concrete Bench & Planters | 1 | 0 | 01-Jul-14 A | 09-Jul-14 A | |
| I-5024 | RFI 586 - Bench Support at Porte Cochere (related to | 1 | 0 | 01-Jul-14 A | 09-Jul-14 A | |
| L10-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7102 | Install Vertical Heat Pump | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L03-7116 | Frame Walls | 1 | 0 | 02-Jul-14 A | 14-Jul-14 A | |
| L03-7118 | Install HM Door Frame | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L04-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L05-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L07-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L08-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L09-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |

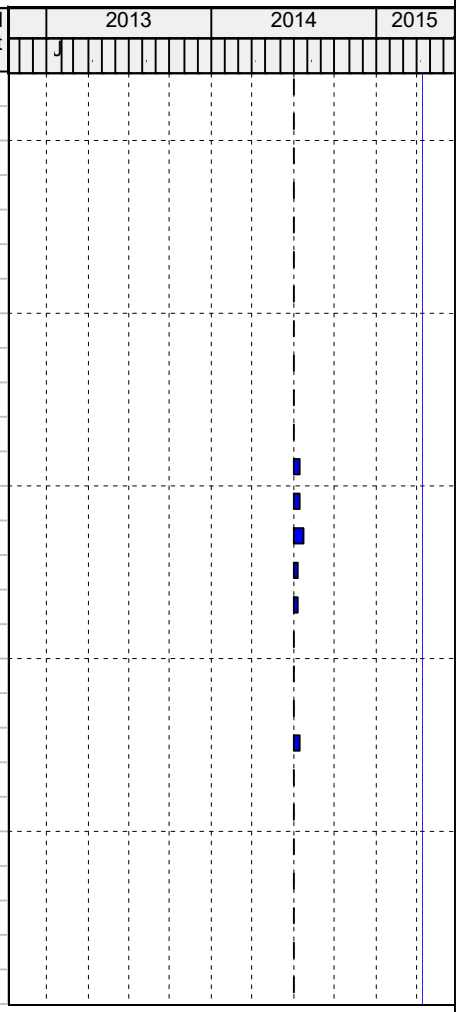



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L12-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| I-3906 | Ballroom Parapet Height Issue/ frame parapet | 1 | 0 | 02-Jul-14 A | 21-Jul-14 A | |
| L06-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| I-3708 | Complete wall framing at Stair/Elevator 5 (LL3) | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L11-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 03-Jul-14 A | 07-Jul-14 A | |
| L04-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L05-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L06-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L07-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L08-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L17-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L10-6040 | Test Heat Pumps - L7, L8, L9 and L10 | 3 | 0 | 07-Jul-14 A | 09-Jul-14 A | |
| L10-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L03-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |

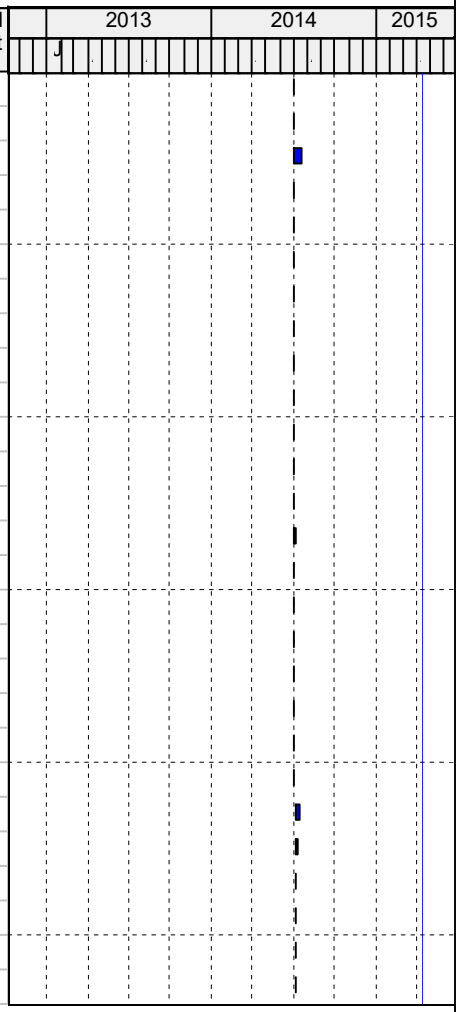


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L04-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L05-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L06-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L07-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L08-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L09-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L10-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L12-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L14-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L11-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Jul-14 A | 29-Jul-14 A | |
| L03-8602 | L3 Pool - Fire Sprinkler R/I | 5 | 0 | 08-Jul-14 A | 22-Jul-14 A | |
| L03-7016 | Install HM door frame | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L11-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L16-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 09-Jul-14 A | |
| L04-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |

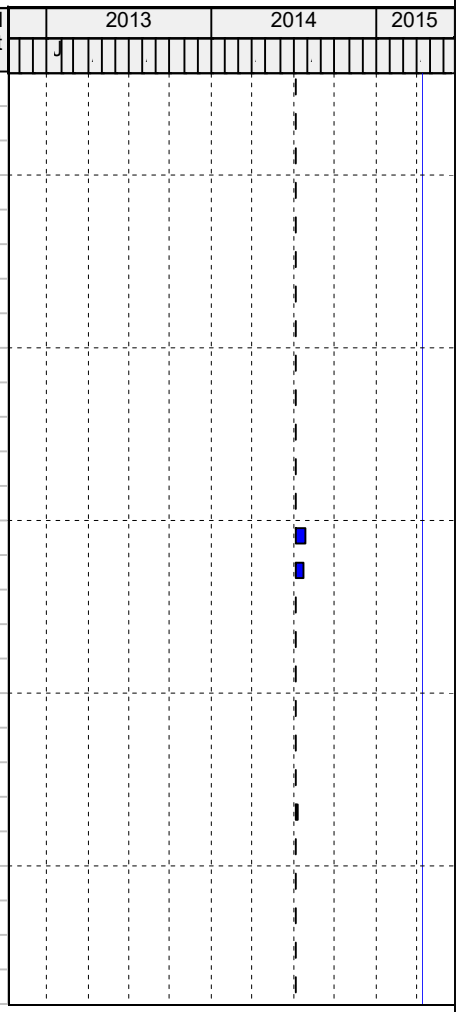



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L12-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| MP-FAB1 | Fabricate and Deliver Bronze Gold Horizontal Panels | 30 | 0 | 09-Jul-14 A | 15-Jul-14 A | |
| L04-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L05-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L06-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L16-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| MP-FAB2 | Fabricate and Deliver Silver Vertical Panels | 45 | 0 | 10-Jul-14 A | 25-Aug-14 A | |
| ASI27capt | ASI No. 27 - City Approved ASI No. 27 (Tower Plumbi | 0 | 0 | 10-Jul-14 A | | |

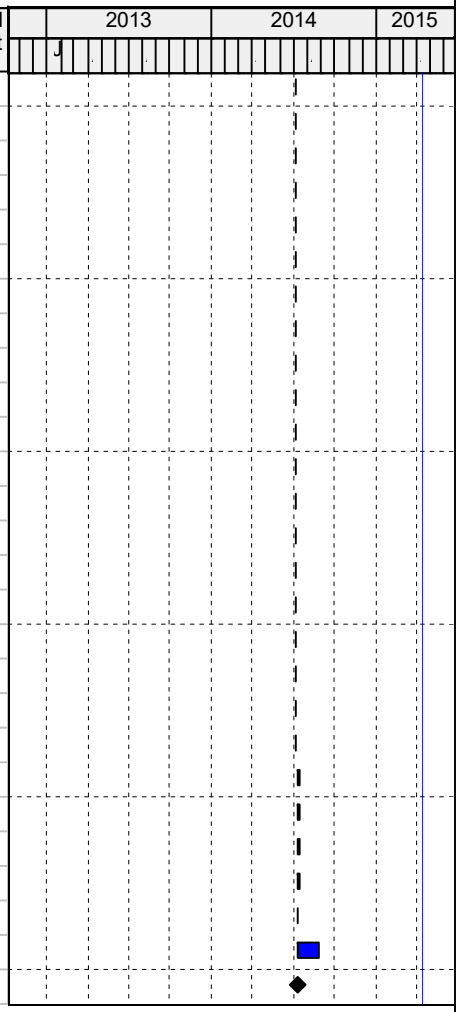



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ASI27cam | ASI No. 27 - City Approved ASI No. 27 (Mechanical) | 0 | 0 | 10-Jul-14 A | | |
| ASI36ca | ASI No. 36 - MDP Electrical Revisions Rev. 16 (City Ap | 0 | 0 | 10-Jul-14 A | | |
| ASI38ca | ASI No. 38 - MDP's Bar & Concierge Plumbing Revisi | 0 | 0 | 10-Jul-14 A | | |
| I-5026 | RFI 611 - Landscaping at Porte Cochere Planters | 1 | 0 | 10-Jul-14 A | 18-Jul-14 A | |
| I-3004 | ASI 38/ Issue ASI 38 | 0 | 0 | 11-Jul-14 A | | |
| I-3006 | ASI 38/ Release bar area for x-ray examination | 5 | 0 | 11-Jul-14 A | 03-Sep-14 A | |
| L07-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| LL1-Z2-6018a | Complete Mech RI at tower crane opening (LL1) | 4 | 0 | 14-Jul-14 A | 17-Jul-14 A | |
| L08-6223 | Frame Corridor Ceilings | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| SW-2006a | Complete Dry Utilities (Phase 2) | 5 | 0 | 14-Jul-14 A | 24-Jul-14 A | |
| L04-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L04-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L05-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L06-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L04-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |

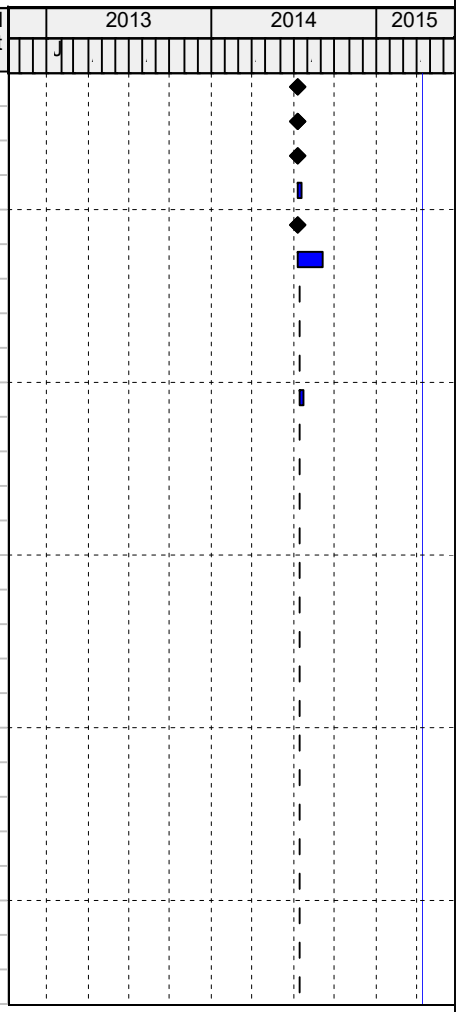



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L11-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L11-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L12-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L12-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L15-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L15-7102 | Install Vertical Heat Pump | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L1B-6026 | Install operable partition steel | 2 | 0 | 15-Jul-14 A | 08-Aug-14 A | |
| L09-6223 | Frame corridor ceilings | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L03-7120 | Electrical Rough-In | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L07-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L07-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L08-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L08-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L09-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L09-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L03-7142 | Install Laundry Chute (All Levels) | 9 | 0 | 15-Jul-14 A | 25-Jul-14 A | |
| LL2-2045 | LL2 - Electrical Room build-out | 15 | 0 | 15-Jul-14 A | 26-Sep-14 A | |
| L03-7122 | HVAC Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |

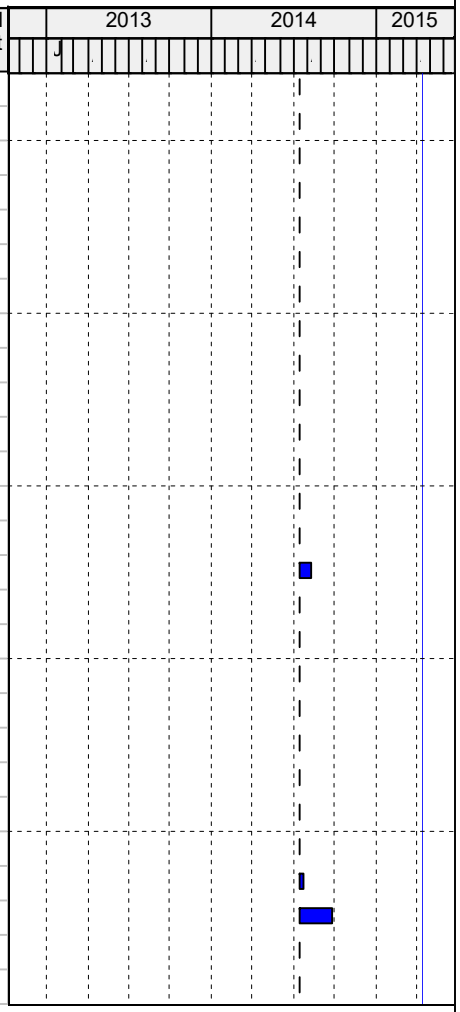



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L05-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L06-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L07-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L07-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L08-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L08-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L09-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L09-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L11-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L11-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L12-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L12-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L15-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L15-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L16-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |

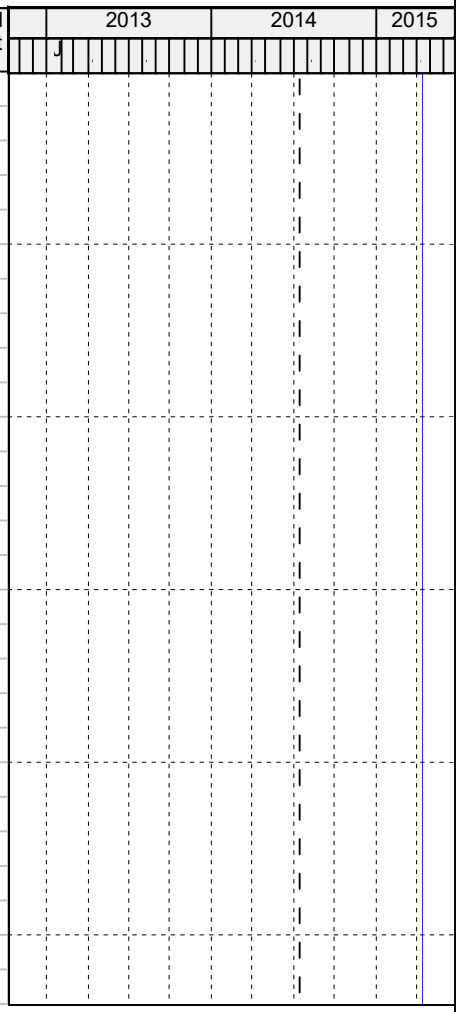



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L17-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| ASI41r1 | ASI No. 41 (Revised) - Kay Lang's Interior Design CD | 0 | 0 | 16-Jul-14 A | | |
| ASI43 | ASI No. 43 - MDP's Electrical Revisions Rev. 19 | 0 | 0 | 16-Jul-14 A | | |
| L03-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L04-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L04-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L05-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L05-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L06-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L06-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L07-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L08-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L09-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L11-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |

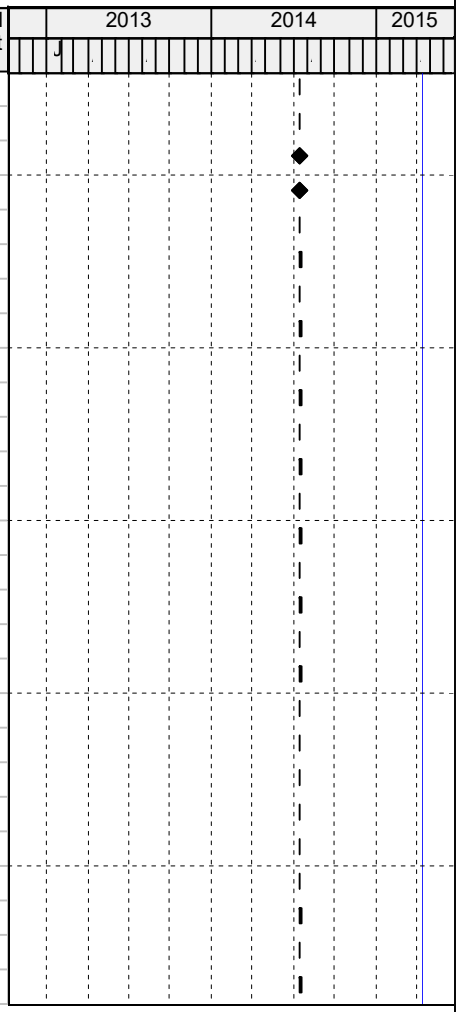



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L12-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L12-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L16-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| ASI42 | ASI No. 42 - JBA's Arch Revs to Lobby and Concierge | 0 | 0 | 17-Jul-14 A | | |
| ASI45 | ASI No. 45 - JBA's Revised Guestroom Suite Layouts | 0 | 0 | 17-Jul-14 A | | |
| L03-8608 | L3 Pool - Electrical R/I | 5 | 0 | 18-Jul-14 A | 10-Nov-14 A | |
| L03-8610 | L3 Pool - Fire Alarm / Elec Specialties R/I | 5 | 0 | 18-Jul-14 A | 10-Nov-14 A | |
| L15-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L15-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| L17-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L17-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| LL2-2052 | LL2 - Install fuel piping and exhaust duct to Generatc | 8 | 0 | 21-Jul-14 A | 15-Aug-14 A | |
| L04-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L04-7016 | Install HM door frame | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L07-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L08-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L10-7116 | Frame Walls | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L16-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 21-Jul-14 A | 22-Jul-14 A | |
| L16-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L17-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| ASI41r2 | ASI No. 41 (Revised) - Kay Lang's Interior Design Spe | 0 | 0 | 22-Jul-14 A | | |
| ASI44 | ASI No. 44 - MDP's Mechanical Revisions Rev. 17 | 0 | 0 | 24-Jul-14 A | | |
| MPT-1002 | Tower - Install Elevation 35 (east elevation-south half) | 8 | 0 | 25-Jul-14 A | 04-Aug-14 A | |
| L16-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 25-Jul-14 A | 25-Jul-14 A | |
| L11-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |

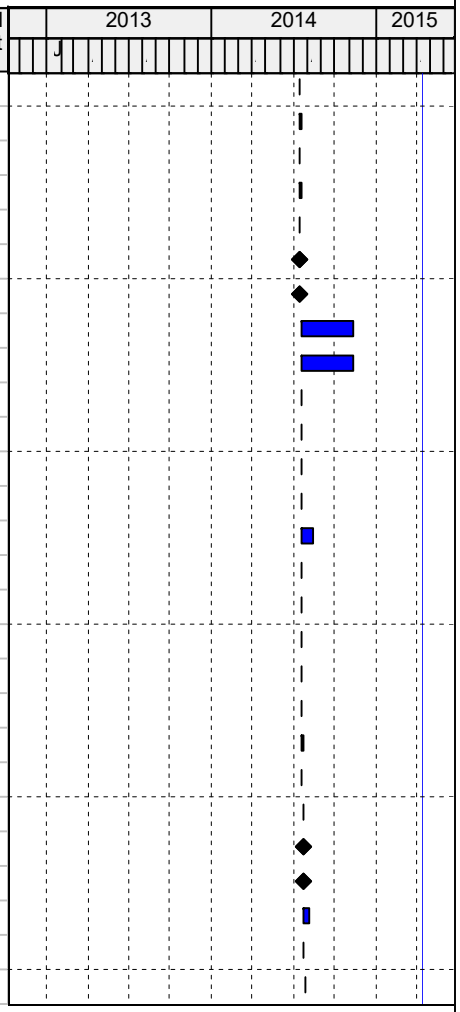


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L14-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L15-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L16-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L10-6223 | Frame Corridor Ceilings | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L11-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L15-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L15-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L11-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L14-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L16-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| I-1304 | Prep Kitchen - Additional framing (ASI 30) | 2 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-2302 | Framing "Go Back" work at LL1 for RFI 233 | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| I-2502 | Electrical rework at LL1 for ASIs 7, 9r2, 14, 27 | 4 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| L12-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L1B-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 01-Aug-14 A | 15-Aug-14 A | |
| MPL4-1000 | Upper L4 Ballroom - Install Elevations 1, 2 & 3 (south | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1000 | Tower - Install Elevations 26-27 (west elevation) [DEL | 13 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPP-1002 | Podium - Install Elevations 1 & 2 (west elevation, sou | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPP-1008 | Podium - Install Elevations 7 & 8 (north & east elevati | 9 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1002 | Upper L4 Ballroom - Install Elevation 10 (west elevatio | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1004 | Upper L4 Ballroom - Install Elevation 9 (north elevatio | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |

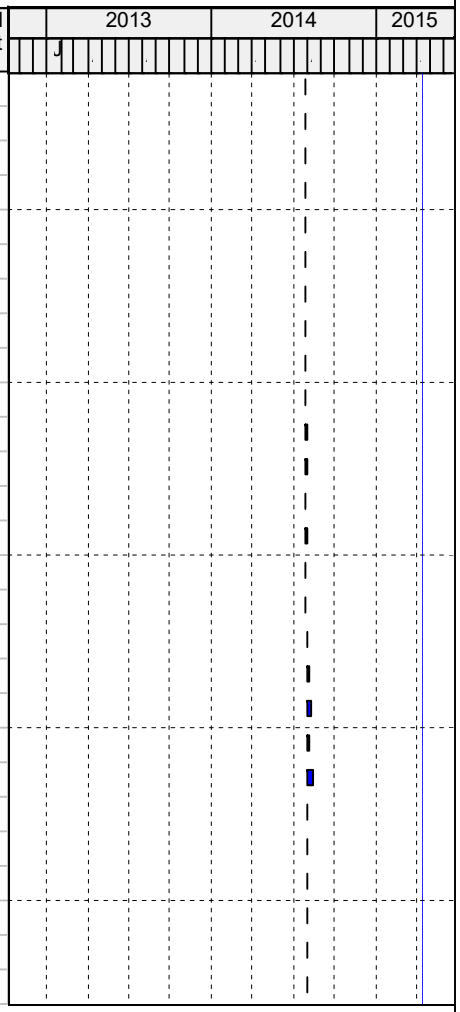



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPT-1006 | Tower - Install Elevation 40 (east return-east end) [DE | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1010 | Tower - Install Elevations 51 (north elevation) [DELET | 8 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-4004 | East Stitched - Install metal panels [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L11-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L11-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L15-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L14-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L17-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| MPT-1010b | Tower - Install Elevation 45 [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| ASI46 | ASI No. 46 - Concept Services Revised Kitchen Drawi | 0 | 0 | 01-Aug-14 A | | |
| L16-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 04-Aug-14 A | 05-Aug-14 A | |
| L11-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Aug-14 A | 08-Aug-14 A | |
| L04-7020 | HVAC Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |

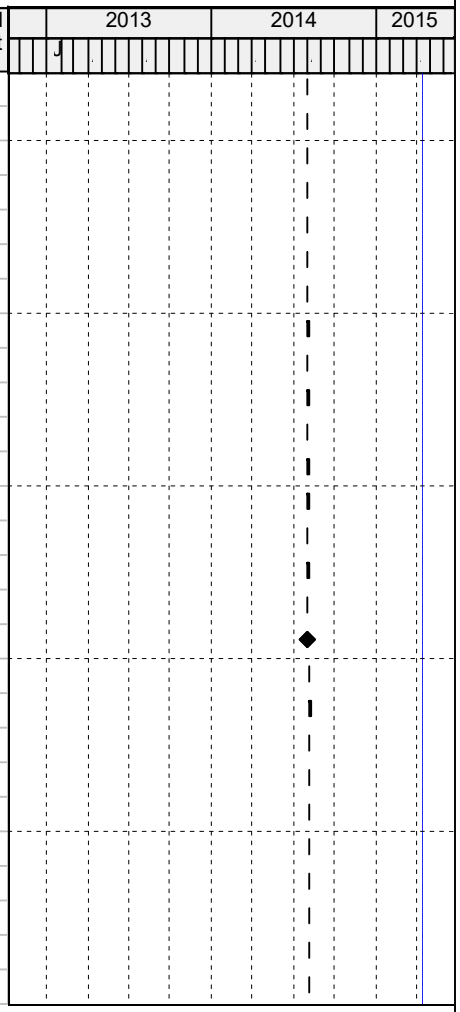



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L14-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L15-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 05-Aug-14 A | 07-Aug-14 A | |
| L05-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L06-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L07-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L08-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L09-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L10-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7018 | Electrical Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L14-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 05-Aug-14 A | 06-Aug-14 A | |
| L14-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| I-4104 | Install added trap primers - LL1 | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L06-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L07-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L08-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L09-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L10-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7020 | HVAC Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |

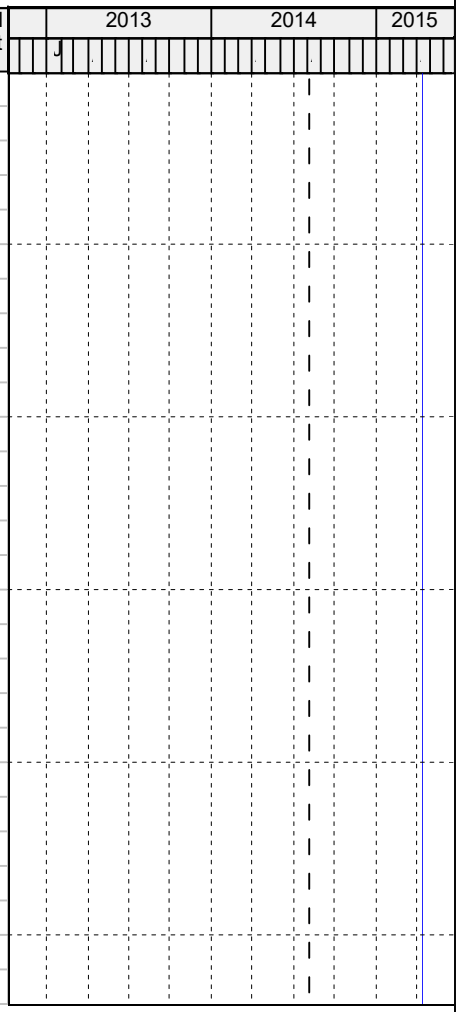



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L16-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| EL-1220 | Elevator fronts delivered | 0 | 0 | 07-Aug-14 A | | |
| L12-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L12-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-6223 | Frame Corridor Ceilings | 4 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L11-7016 | Install HM door frame | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L12-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L15-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L15-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L16-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L16-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L17-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L17-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| ASI48 | ASI No. 48 - MDP Revisions to Electrical & Plumbing | 0 | 0 | 08-Aug-14 A | | |
| L14-6040 | Test Heat Pumps - L11, L12 and L14 | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| PH-6026 | PH - Insulation/Vapor Barrier/GWB at Exterior Walls | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| L11-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L11-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |

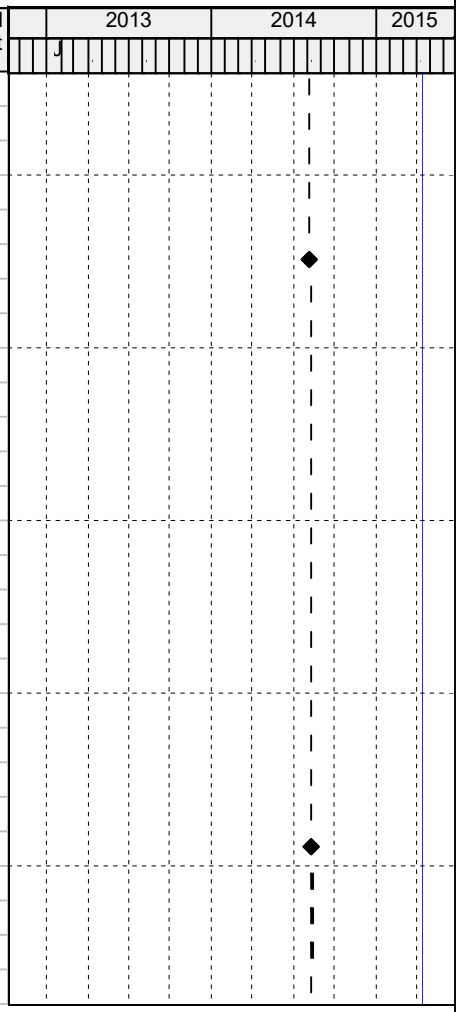



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7026 | Inspections for GWB Cover | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 13-Aug-14 A | 13-Aug-14 A | |
| L15-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 14-Aug-14 A | 15-Aug-14 A | |
| LL2E-8108 | LL2 - Set fire pumps and equipment | 5 | 0 | 14-Aug-14 A | 29-Sep-14 A | |
| L10-7028 | GWB Hang/Tape/Finish | 5 | 0 | 14-Aug-14 A | 05-Dec-14 A | |
| L12-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L12-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L16-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L1BOH2-6008 | Int Wall Framing & Inspection | 5 | 0 | 14-Aug-14 A | 20-Aug-14 A | |
| I-4106 | Install added trap primers - L1 | 1 | 0 | 15-Aug-14 A | 15-Aug-14 A | |
| L14-6223 | Frame Corridor Ceilings | 4 | 0 | 15-Aug-14 A | 16-Aug-14 A | |
| L03-8136 | Install Counter Subtops | 3 | 0 | 15-Aug-14 A | 18-Aug-14 A | |
| LL2-2054 | LL2 - GWB, Hang 1st Layer at Laundry Room | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| LL2E-8112 | LL2 - Form/Pour Fire Pump Pads/Curbs | 2 | 0 | 16-Aug-14 A | 18-Aug-14 A | |
| LL1-6014Ia | L1 bar redesign - rework plumbing at ceilings | 10 | 0 | 18-Aug-14 A | 05-Jan-15 A | |
| L15-6223 | Frame Corridor Ceilings | 4 | 0 | 18-Aug-14 A | 21-Aug-14 A | |
| L17-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |

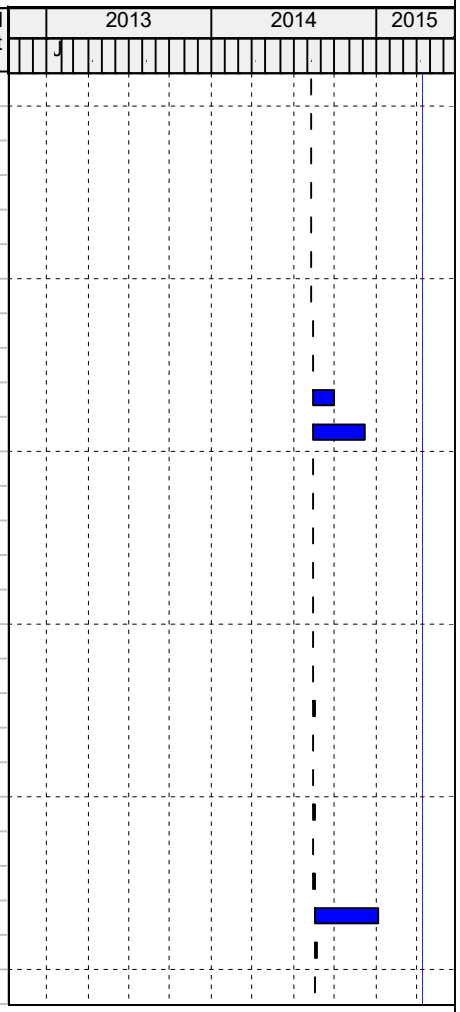



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Aug-14 A | 18-Aug-14 A | |
| L04-8136 | Install Counter Subtops | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-6014Ic | L1 bar redesign - rework electrical at ceilings | 10 | 0 | 18-Aug-14 A | 05-Jan-15 A | |
| LL2E-8114 | LL2 - Set Tube Steel at Door | 1 | 0 | 19-Aug-14 A | 19-Aug-14 A | |
| L17-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 20-Aug-14 A | 21-Aug-14 A | |
| L17-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 20-Aug-14 A | 20-Aug-14 A | |
| L05-8136 | Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 26-Aug-14 A | |
| L06-8136 | Bathrooms - Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 13-Oct-14 A | |
| L16-6223 | Frame Corridor Ceilings | 4 | 0 | 21-Aug-14 A | 29-Aug-14 A | |
| L17-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 21-Aug-14 A | 22-Aug-14 A | |
| L17-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 21-Aug-14 A | 21-Aug-14 A | |
| L1BOH2-6016 | Electrical RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6018 | HVAC RI | 4 | 0 | 21-Aug-14 A | 17-Oct-14 A | |
| L15-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7020 | HVAC Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7022 | Fire Sprinkler Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| LL2E-8116 | LL2 - Set Door Jamb | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| ASI49 | ASI No. 49 - SCA Transformer Vault Alcove Connectic | 0 | 0 | 22-Aug-14 A | | |
| L03-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L04-7028 | GWB Hang/Tape/Finish | 5 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L05-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L05-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L06-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L06-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |

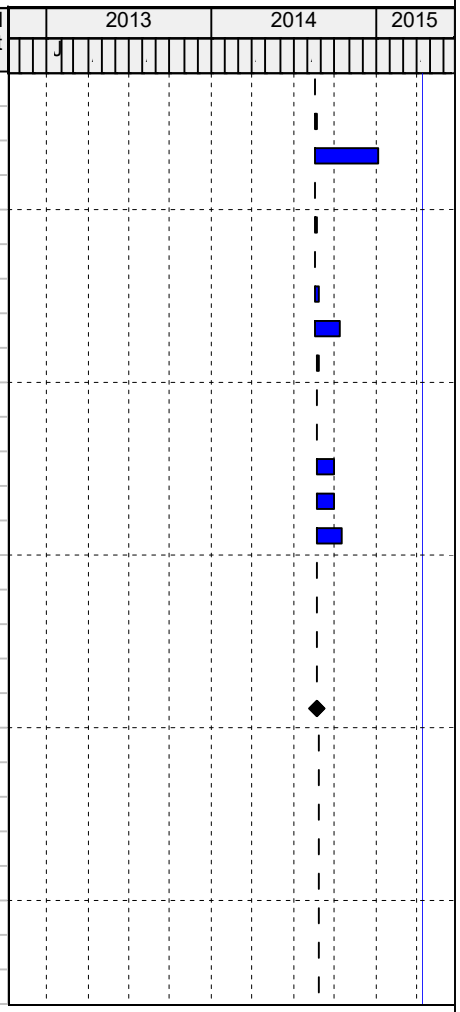



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L03-8123 | Bathroom "Barn Doors" On Site | 0 | 0 | 25-Aug-14 A | | |
| LL3-6026 | LL3 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL2-6026 | LL2 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL1-Z3-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L1BOH2-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L02-6026 | L2 - Set Elevator Fronts (Cars 1-4 | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |

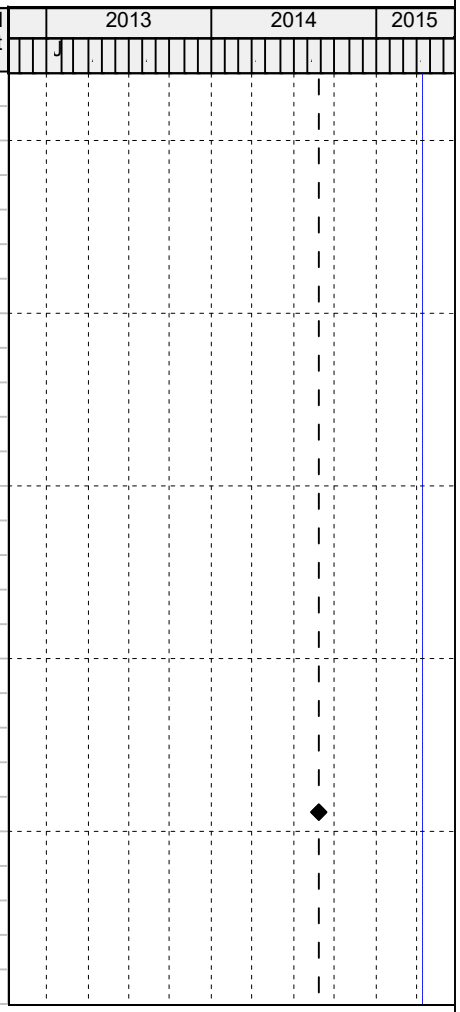



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L04-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L05-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L06-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L07-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L08-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L09-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L10-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L11-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L12-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L14-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L15-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L16-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L17-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| MPT-1008 | Tower - Install E/W Wing, N. Side West Half (Elev 50,: | 7 | 0 | 26-Aug-14 A | 03-Oct-14 A | |
| L06-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L07-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L08-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L05-7026 | Inspections for GWB Cover | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L05-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L11-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 08-Dec-14 A | |
| L12-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L14-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L03-8105a | Painting - Split Door Jambs | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L09-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L10-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L11-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |

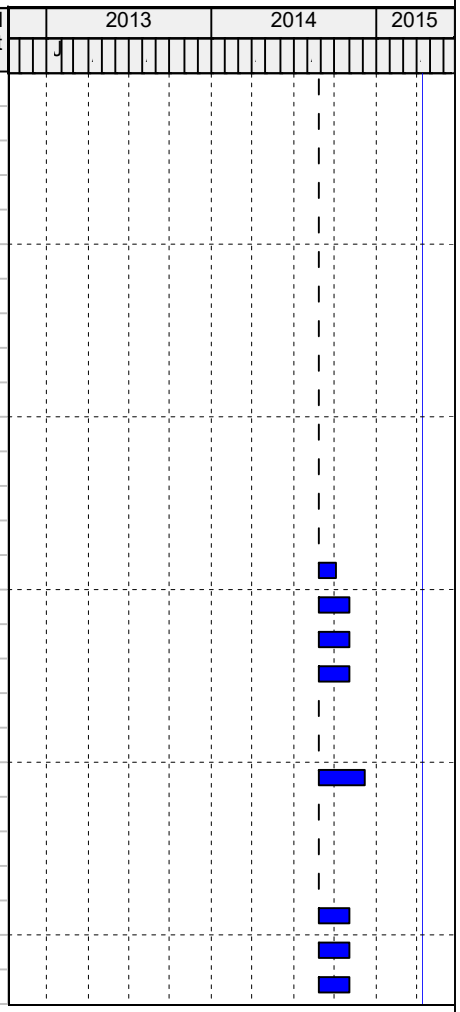



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L14-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L15-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L16-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L05-8201 | Install ACT Grid @ Corridors | 2 | 0 | 27-Aug-14 A | 28-Aug-14 A | |
| L16-7022 | Fire Sprinkler Rough-In | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L04-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L06-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| EP-5110a | L1 - Install Steel at Revolving Door Opening | 3 | 0 | 27-Aug-14 A | 29-Aug-14 A | |
| L05-8105a | Painting - Split Door Jambs | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| ASI50 | ASI No. 50 - Updated S1 Plumbing Fixture | 0 | 0 | 28-Aug-14 A | | |
| I-4102 | Install added trap primers - LL2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4108 | Install added trap primers - L2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4110 | Install added trap primers - L3 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4112 | Install added trap primers - Roof PH | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| L03-8124d | Flooring On Site and Acclimated | 2 | 0 | 29-Aug-14 A | 01-Sep-14 A | |
| ASI47 | ASI No. 47 - Architectural and Interior Design Revisior | 0 | 0 | 29-Aug-14 A | | |
| L02-5102 | L2 - Storefront Frames | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| L04-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L05-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L17-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L03-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L12-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L14-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L07-8136 | Install Counter Subtops | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| LL1-Z3-FCC10 | FCC - Set Jamb | 1 | 0 | 02-Sep-14 A | 03-Sep-14 A | |
| MPT-1004 | Tower - Install E/W Wing, S. Side w/o Windows (Elev | 10 | 0 | 03-Sep-14 A | 17-Oct-14 A | |

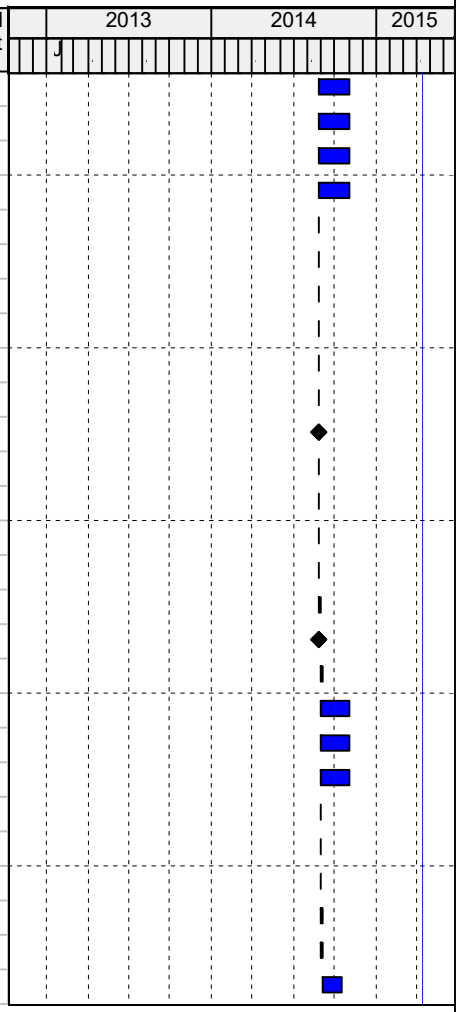


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-7028 | GWB Hang/Tape/Finish | 5 | 0 | 03-Sep-14 A | 02-Dec-14 A | |
| L12-7028 | GWB Hang/Tape/Finish | 5 | 0 | 03-Sep-14 A | 08-Dec-14 A | |
| L03-8126a | Doors & Hardware On Site | 0 | 0 | 03-Sep-14 A | | |
| LL1-Z3-FCC12 | FCC - Sheetrock Outside Wall | 1 | 0 | 03-Sep-14 A | 03-Sep-14 A | |
| ASI46r1 | ASI No. 46 (Revised) - Revised Kitchen Equipment M | 0 | 0 | 03-Sep-14 A | | |
| L16-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| L17-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Sep-14 A | 11-Sep-14 A | |
| L02-5104b | L2 - Install Storefront Temporary Enclosures | 1 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| LL1-Z3-FCC14 | FCC - Verify Fire Caulk OK & Inspect Room OK to 2n | 1 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| I-3008 | ASI 38/ Coordinate and perform x-ray examination | 7 | 0 | 04-Sep-14 A | 24-Sep-14 A | |
| L02-5104a | L2 - Measure/Fabricate Storefront Glazing | 15 | 0 | 05-Sep-14 A | 18-Sep-14 A | |
| LL1-Z3-FCC16 | FCC - GWB, Hang 2nd Layer | 2 | 0 | 05-Sep-14 A | 08-Sep-14 A | |
| ASI52 | ASI No. 52 - MDP Electrical Revisions Rev. 21 | 0 | 0 | 05-Sep-14 A | | |
| I-5028 | RFI 687 - Planter at Porte Cochere Grid V & 25 | 1 | 0 | 05-Sep-14 A | 10-Sep-14 A | |
| L03-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L15-7018 | Electrical Rough-In | 1 | 0 | 08-Sep-14 A | 08-Sep-14 A | |
| EL-1228 | Construct/Approve elevator lobby framing mockup (L | 3 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| LL2E-8118 | LL2 - Frame Infill, Install Densglass & Inspect at Fire I | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L06-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L08-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L15-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7018 | Electrical Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L3-5104a | L3 - Measure/Fabricate Storefront Glazing | 15 | 0 | 09-Sep-14 A | 30-Sep-14 A | |
| L03-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 23-Sep-14 A | |

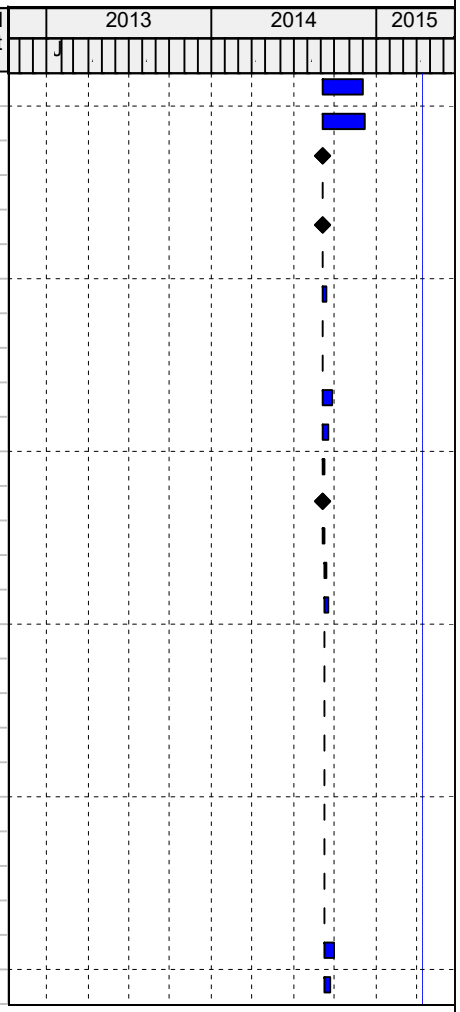



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L04-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L06-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| L08-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| L05-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L06-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L06-7028 | GWB Hang/Tape/Finish | 5 | 0 | 10-Sep-14 A | 02-Dec-14 A | |
| L08-7028 | GWB Hang/Tape/Finish | 5 | 0 | 10-Sep-14 A | 05-Dec-14 A | |
| L15-7026 | Inspections for GWB Cover | 1 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| LL2E-8120 | LL2 - Insulation, Vapor Barrier & Inspect at Fire Pump | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| ASI53 | ASI No. 53 - Pool Chemical Storage System | 0 | 0 | 10-Sep-14 A | | |
| L08-8395 | Framing at Elevator Lobby | 4 | 0 | 11-Sep-14 A | 17-Sep-14 A | |
| L15-7028 | GWB Hang/Tape/Finish | 5 | 0 | 11-Sep-14 A | 08-Dec-14 A | |
| L08-8136 | Install Counter Subtops | 3 | 0 | 11-Sep-14 A | 16-Sep-14 A | |
| L02-6025 | L2 - Framing Go-Back Work (left out for mechanical e | 4 | 0 | 11-Sep-14 A | 02-Oct-14 A | |
| L1-5104a | L1 - Measure/Fabricate Storefront Glazing | 15 | 0 | 12-Sep-14 A | 18-Sep-14 A | |
| L1B-8102c | Finish framing and MEP at Main Ballroom East Wall ( | 10 | 0 | 12-Sep-14 A | 02-Oct-14 A | |
| L09-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L10-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L11-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L12-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L16-7026 | Inspections for GWB Cover | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| MPT-1014 | Tower - Install E/W Wing, N. Side, E. Half (Elev 46-49 | 8 | 0 | 15-Sep-14 A | 28-Oct-14 A | |
| LL2-6032 | LL2 - Complete Framing (Including Elevator Lobby) | 4 | 0 | 15-Sep-14 A | 18-Sep-14 A | |
| L1-5104b | L1 - Install Storefront Temporary Enclosures | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| LL1-Z3-FCC18 | FCC - Install Temp Door | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |

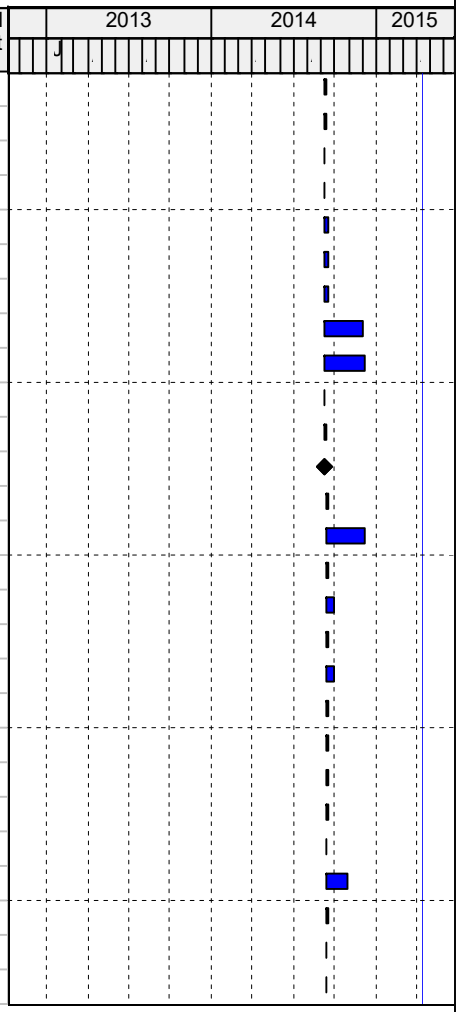



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2058a | LL2 - GWB Hang 1st Layer | 5 | 0 | 15-Sep-14 A | 19-Sep-14 A | |
| LL2-2064 | LL2 - Generator Room - Finish Exhaust Piping | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| I-3010 | ASI 38/ Prepare proposal for MEP relocations | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| ASI51 | ASI No. 51 - Interior Design Revisions | 0 | 0 | 15-Sep-14 A | | |
| L16-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L07-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L09-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L10-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L14-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L15-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L03-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| L16-7028 | GWB Hang/Tape/Finish | 5 | 0 | 16-Sep-14 A | 08-Dec-14 A | |
| L17-7018 | Electrical Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L09-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L10-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| LL3-6028 | LL3 - Frame Elevator Lobby | 2 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| LL4-6026 | LL4 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| I-3012 | ASI 38/ Owner approve proposal for MEP relocations | 3 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| ASI50r1 | ASI No. 50 (Revised) - Updated Plumbing Fixtgure K | 0 | 0 | 16-Sep-14 A | | |
| L11-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L12-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L14-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L15-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L04-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L17-7026 | Inspections for GWB Cover | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L17-7116 | Frame Walls | 4 | 0 | 17-Sep-14 A | 29-Sep-14 A | |

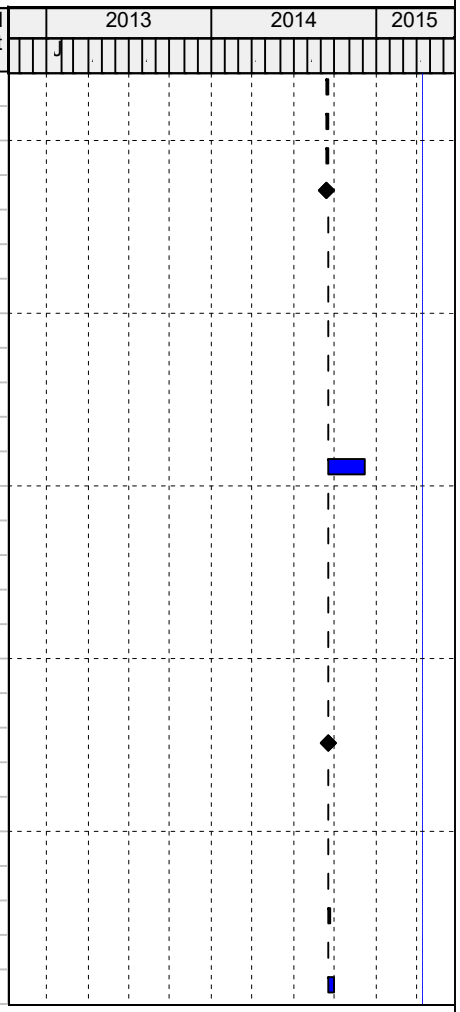



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2066 | LL2 - Generator Room - Finish Fuel Piping | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L16-8395 | Framing at Elevator Lobby | 4 | 0 | 18-Sep-14 A | 26-Sep-14 A | |
| L02-5104 | L2 - Storefront Glazing | 2 | 0 | 18-Sep-14 A | 22-Sep-14 A | |
| L17-7028 | GWB Hang/Tape/Finish | 5 | 0 | 18-Sep-14 A | 08-Dec-14 A | |
| LL4-6028 | LL4 - Frame Elevator Lobby | 2 | 0 | 18-Sep-14 A | 02-Oct-14 A | |
| MPT-1010a | Tower - Install E/W Wing, West End (Elev 52,53) | 8 | 0 | 18-Sep-14 A | 10-Oct-14 A | |
| ASI44ca | ASI No. 44 - MDP's Mechanical Revisions Rev. 17 (Ci | 0 | 0 | 18-Sep-14 A | | |
| LL2-2068 | LL2 - Generator Room - Electrical Finishes | 3 | 0 | 19-Sep-14 A | 30-Sep-14 A | |
| L07-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L09-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L04-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L05-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L03-8140 | Countertops On Site | 0 | 0 | 22-Sep-14 A | | |
| L03-8129a | Shower Doors On Site | 0 | 0 | 22-Sep-14 A | | |
| LL1-Z3-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L1BOH2-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2-2048a | LL2 - Move in Laundry Room Ironer | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2E-8122 | LL2 - Hang GWB at Fire Pump Room | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-FCC20 | FCC - Rough-In and Install Panels | 25 | 0 | 22-Sep-14 A | 21-Nov-14 A | |
| I-3014 | Core drill for MEP relocations | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L05-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L07-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 05-Dec-14 A | |
| L09-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 05-Dec-14 A | |
| L14-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 08-Dec-14 A | |
| L04-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L05-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L06-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |

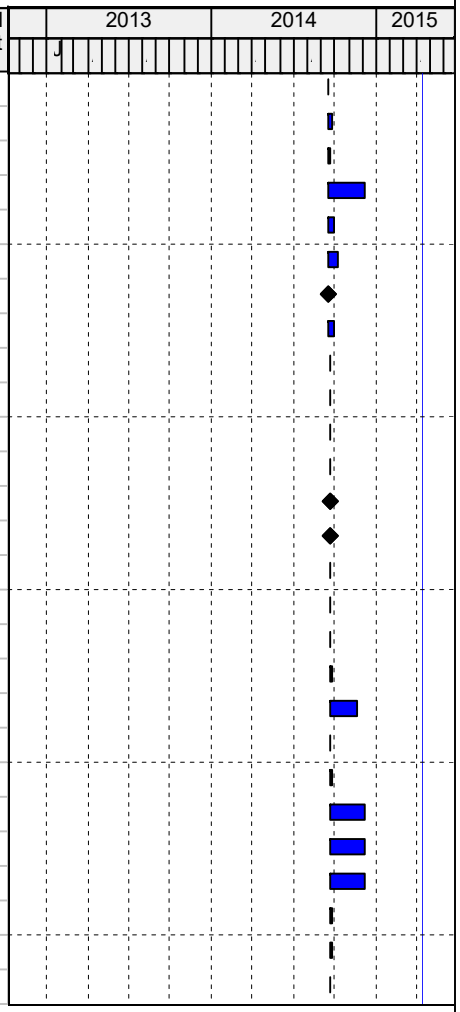



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| ASI53ca | ASI No. 53 - Pool Chemical Storage System (City Apr | 0 | 0 | 23-Sep-14 A | | |
| L04-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L06-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L04-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L05-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-7122 | HVAC Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| LL2-2058 | LL2 - Tape/Finish Laundry Room | 3 | 0 | 24-Sep-14 A | 26-Sep-14 A | |
| I-5034 | RFI 717 - Porte Cochere Paving Details | 1 | 0 | 24-Sep-14 A | 29-Oct-14 A | |
| L08-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L17-8395 | Framing at Elevator Lobby | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L05-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L06-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L07-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L08-7120 | Electrical Rough-In | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| LL2E-8124 | LL2 - Temp-In Louver Opening at Fire Pump Room | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L1-5104c | L1 - Install Storefront at Main Entry Facade | 5 | 0 | 25-Sep-14 A | 10-Oct-14 A | |
| I-5030 | RFI 715 - Additional Site Paving Per City | 1 | 0 | 25-Sep-14 A | 14-Oct-14 A | |
| L16-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L08-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |

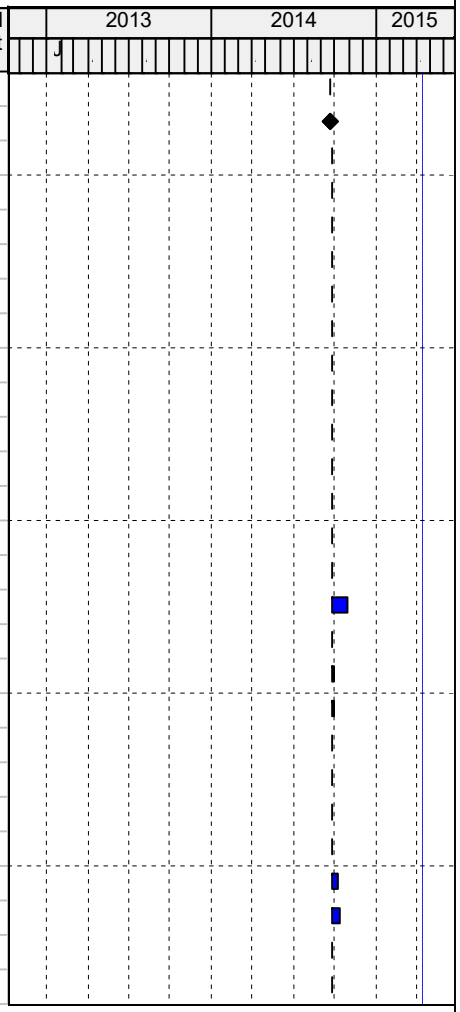



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L10-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L16-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L17-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L17-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L09-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L09-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L11-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L12-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L14-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L15-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L17-7118 | Install HM Door Frame | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| LL3-6030 | LL3 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL4-6030 | LL4 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL2-6034 | LL2 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L1BOH2-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L02-6030 | L2 - Framing at Elevator Lobby & North Half | 4 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| MPT-1022 | Tower - Caulking, west | 8 | 0 | 29-Sep-14 A | 03-Nov-14 A | |
| PH-6015 | PH - Set Boilers and Pumps | 12 | 0 | 29-Sep-14 A | 15-Oct-14 A | |
| L11-8204 | Bathrooms - Vinyl Wall Coverings | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L10-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L17-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L11-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |

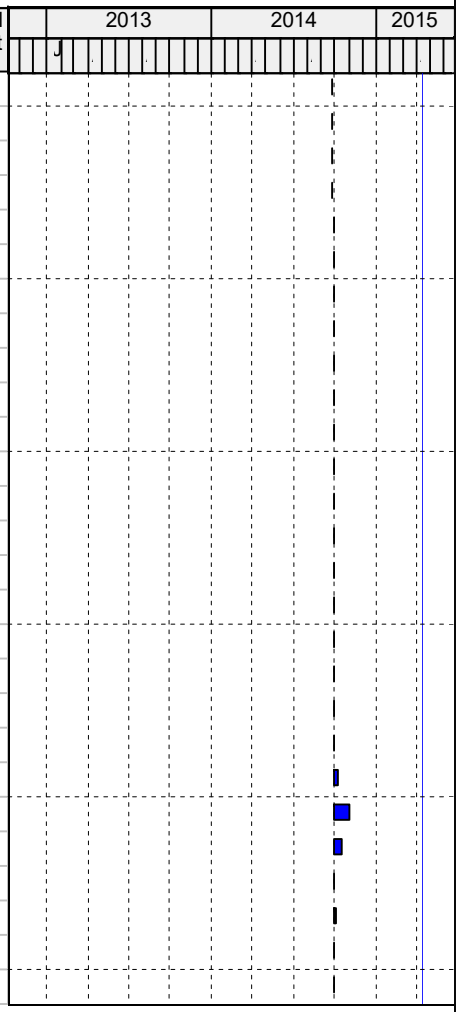



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L07-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 30-Sep-14 A | 08-Oct-14 A | |
| L11-8201 | Install ACT Grid @ Corridors | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L09-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L09-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L11-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L12-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L14-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L15-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| LL2-2072 | Generator - Complete generator and annunciator cor | 5 | 0 | 30-Sep-14 A | 21-Oct-14 A | |
| L17-6040 | Test Heat Pumps - L16 and L17 | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L17-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L14-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L03-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |

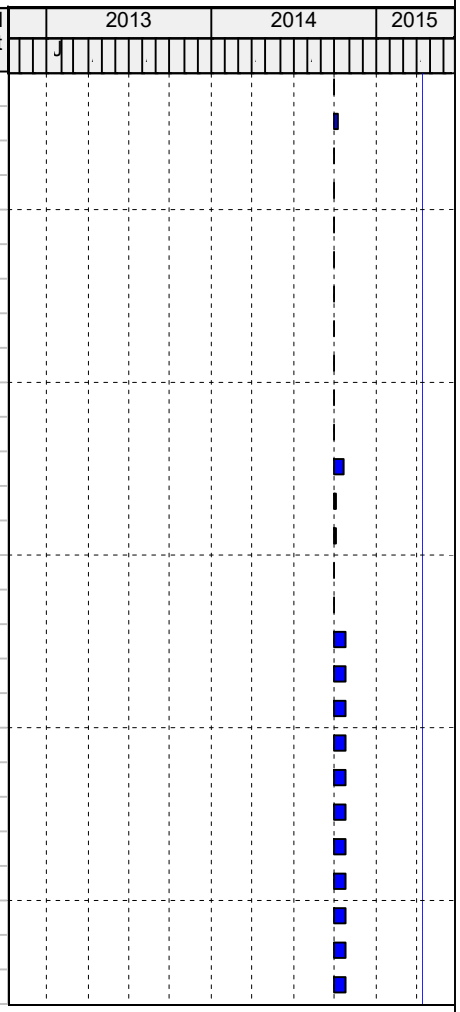



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L11-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |

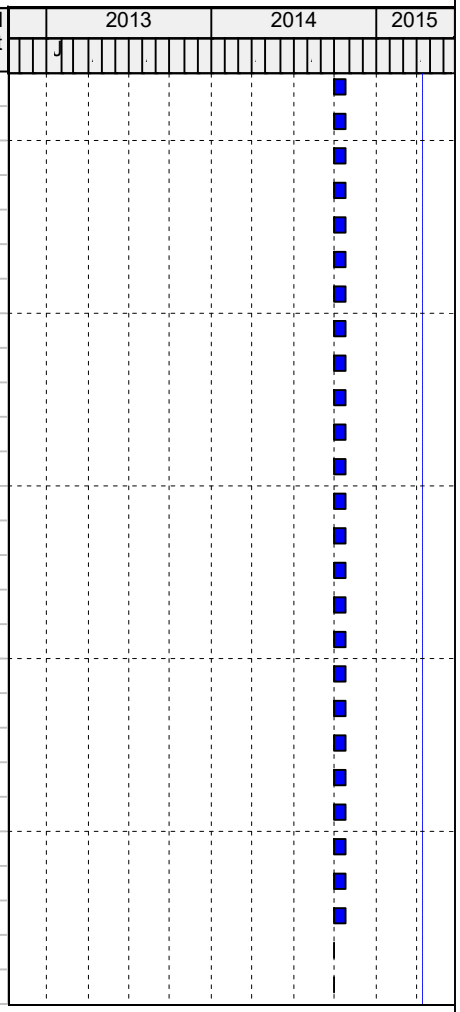



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L12-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L14-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L16-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L17-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L09-8136 | Install Counter Subtops | 3 | 0 | 01-Oct-14 A | 03-Oct-14 A | |
| L02-6032 | L2 - Electrical RI at Elevator Lobby & North Half | 5 | 0 | 01-Oct-14 A | 08-Oct-14 A | |
| SW-2306 | Prep, grind and overlay at 11th Ave, 3rd Place & 2nd | 5 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 01-Oct-14 A | 16-Dec-14 A | |
| L16-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L14-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L15-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1BOH2-8130 | Inspections For Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L02-6024a | L2 - Inspections - South Half | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L06-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| L17-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| LL2-2074 | Generator - Install fuel fill | 2 | 0 | 03-Oct-14 A | 06-Oct-14 A | |
| L07-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| MPT-1020 | Tower - Install E/W Wing, East End (Elev 41,44) | 5 | 0 | 06-Oct-14 A | 18-Oct-14 A | |
| LL1-8102a | GWB Hang/Tape (Ceilings) | 10 | 0 | 06-Oct-14 A | 18-Nov-14 A | |
| L1BOH2C-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |

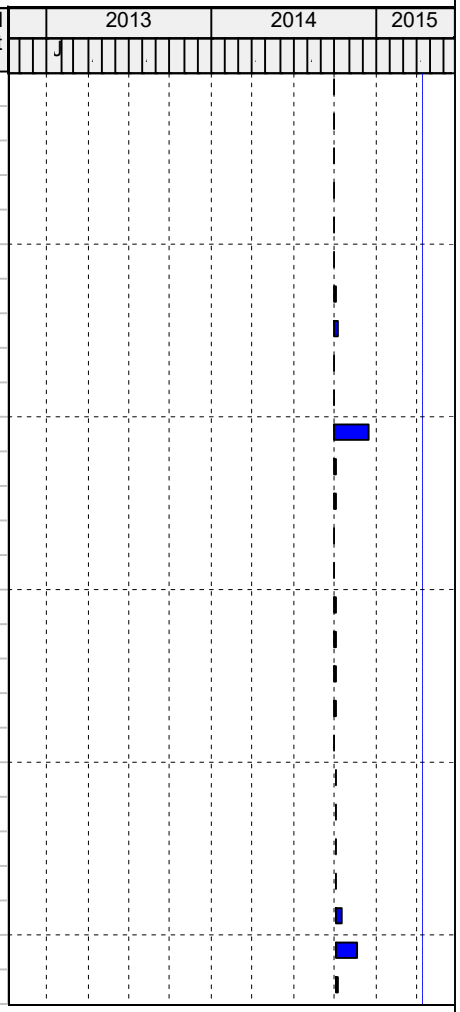



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1BOH2C-6014 | Complete Plumbing RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6016 | Complete Electrical RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6018 | Complete HVAC RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L03-8200a | New murals on site (date estimated) | 0 | 0 | 06-Oct-14 A | | |
| SW-2100 | Zone 1 - Survey curb & site lighting | 2 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 06-Oct-14 A | 06-Oct-14 A | |
| L1BOH2-8100 | Insulation | 4 | 0 | 07-Oct-14 A | 13-Oct-14 A | |
| L17-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L12-8201 | Install ACT Grid @ Corridors | 2 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| L10-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 07-Oct-14 A | 20-Oct-14 A | |
| L03-8216x | Vinyl Wall Coverings - Install Murals | 2 | 0 | 07-Oct-14 A | 29-Dec-14 A | |
| L1B-8102b | GWB Hang (Walls) & Inspection - Exterior Wall at Cor | 3 | 0 | 07-Oct-14 A | 09-Oct-14 A | |
| RF-4048 | Tower Roof - Install davit arms | 3 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| LL2-2076 | Generator - Install fuel fill mechanical piping | 4 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L12-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L09-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L03-8633 | Pool - Install waterproofing & test | 3 | 0 | 08-Oct-14 A | 17-Oct-14 A | |
| L03-8130 | Install Door Hardware | 3 | 0 | 08-Oct-14 A | 28-Oct-14 A | |
| L10-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L02-8102a | L2 - GWB Hang / Tape / Finish - South Half | 7 | 0 | 09-Oct-14 A | 27-Oct-14 A | |
| SW-2102 | Zone 1 - Vacate SE corner | 2 | 0 | 09-Oct-14 A | 11-Oct-14 A | |
| SW-2106 | Zone 1 - Sawcut and remove asphalt | 4 | 0 | 09-Oct-14 A | 14-Oct-14 A | |
| L11-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 09-Oct-14 A | |
| SW-2200 | Zone 2 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |
| SW-2300 | Zone 3 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |
| SW-2108 | Zone 1 - Install east footing drain | 4 | 0 | 10-Oct-14 A | 20-Oct-14 A | |

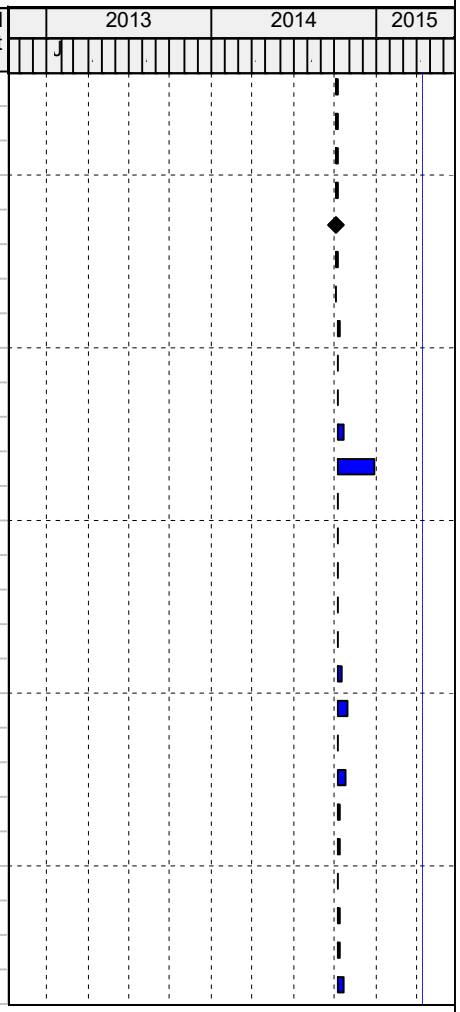



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8130 | Install Door Hardware | 3 | 0 | 10-Oct-14 A | 29-Oct-14 A | |
| ML-5962 | Man/Material Lifts - Remove Roof Lift Stop | 0 | 0 | | 11-Oct-14 A | |
| I-1102 | Additional work at new L17 guest rooms | 5 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| LL2-2046 | LL2 - Generator Room - Misc. Finishes | 3 | 0 | 13-Oct-14 A | 21-Nov-14 A | |
| RF-4008 | Tower Roof - Install corrugated metal panels | 5 | 0 | 13-Oct-14 A | 03-Nov-14 A | |
| MPT-1018b | Tower - Roof cornice frame & sheath | 6 | 0 | 13-Oct-14 A | 24-Oct-14 A | |
| L02-8100a | L2 - Insulation - South Half | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| SW-2112 | Zone 1 - Grade for curb and gutter | 3 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| SW-2202 | Zone 2 - Install site lighting | 5 | 0 | 13-Oct-14 A | 24-Nov-14 A | |
| SW-2204 | Zone 2 - Repave utility trenches | 4 | 0 | 13-Oct-14 A | 22-Oct-14 A | |
| L12-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 13-Oct-14 A | |
| I-5038 | RFI 735 - Landscape Irrigation Conflict | 1 | 0 | 13-Oct-14 A | 03-Nov-14 A | |
| SW-2302 | Zone 3 - Grade for curb and gutter | 2 | 0 | 14-Oct-14 A | 01-Dec-14 A | |
| L14-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 14-Oct-14 A | 16-Oct-14 A | |
| L05-8130 | Install Door Hardware | 3 | 0 | 14-Oct-14 A | 03-Nov-14 A | |
| L14-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 14-Oct-14 A | |
| I-5032 | RFI 715.1 - Additional Site Paving Per City | 1 | 0 | 14-Oct-14 A | 29-Oct-14 A | |
| L16-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L15-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 15-Oct-14 A | 17-Oct-14 A | |
| L15-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 15-Oct-14 A | |
| SW-2206 | Zone 2 - Grade for curb and gutter | 2 | 0 | 16-Oct-14 A | 20-Oct-14 A | |
| I-5598 | Resolve FCC hard lid ceiling issue (RFI 734) | 1 | 0 | 16-Oct-14 A | 16-Nov-14 A | |

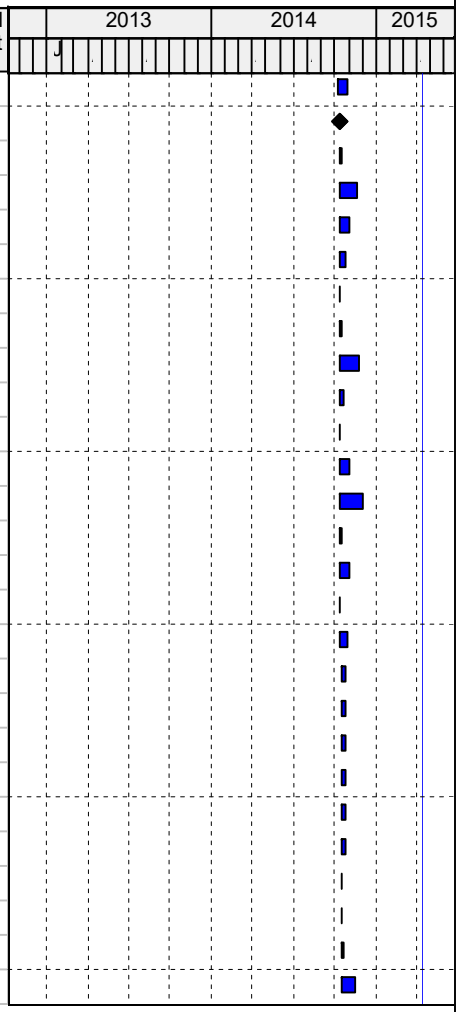



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ASI57 | ASI No. 57 - MDP Electrical Revisions Rev. 22 | 0 | 0 | 17-Oct-14 A | | |
| MPP-1000 | Podium - Install W/S/N Elevations (Elev 1-5, 6,9-19,2 | 10 | 0 | 20-Oct-14 A | 10-Dec-14 A | |
| L06-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 20-Oct-14 A | 23-Oct-14 A | |
| LL2-8106a | LL2, Garage - Pinned Insulation (except at ramp) | 4 | 0 | 20-Oct-14 A | 04-Dec-14 A | |
| L1B-8102d | GWB Hang (Walls) & Inspection - Main Ballroom East | 1 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| SW-2114 | Zone 1 - FRP curb and gutter | 2 | 0 | 20-Oct-14 A | 14-Nov-14 A | |
| RF-4044 | Ballroom Roof - Install metal coping | 3 | 0 | 20-Oct-14 A | 13-Nov-14 A | |
| L08-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 21-Oct-14 A | 23-Oct-14 A | |
| MPT-1018 | Tower - Install Roof Penthouse (Elev 36b,37,38.39) | 5 | 0 | 21-Oct-14 A | 05-Dec-14 A | |
| L11-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2208 | Zone 2 - FRP curb and gutter | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2304 | Zone 3 - FRP curb and gutter | 3 | 0 | 21-Oct-14 A | 02-Dec-14 A | |
| L15-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L06-8130 | Install Door Hardware | 3 | 0 | 21-Oct-14 A | 03-Nov-14 A | |
| I-5100 | Resolve changes (ASI's and RFI's) | 1 | 0 | 21-Oct-14 A | 07-Jan-15 A | |
| L03-8634 | Pool - Install reinforcing steel & inspect | 5 | 0 | 22-Oct-14 A | 30-Oct-14 A | |
| MPT-1016 | Tower - Install N/S Wing, S. End W. of Manlift (Elev 2 | 5 | 0 | 22-Oct-14 A | 05-Dec-14 A | |
| SW-2116 | Zone 1 - Fine grade for sidewalk | 3 | 0 | 22-Oct-14 A | 09-Mar-15 A | |
| LL4-8106 | LL4 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| LL3-8106 | LL3 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L14-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L08-8130 | Install Door Hardware | 3 | 0 | 22-Oct-14 A | 04-Nov-14 A | |
| L07-8130 | Install Door Hardware | 3 | 0 | 22-Oct-14 A | 03-Nov-14 A | |
| ASI54 | ASI No. 54 - Architectural Revisions for Lobby and Cl | 0 | 0 | 22-Oct-14 A | | |
| ASI55 | ASI No. 55 - Kay Lang Interior Concierge and Lobby | 0 | 0 | 22-Oct-14 A | | |
| L03-8606 | L3 Pool - HVAC R/I | 3 | 0 | 23-Oct-14 A | 27-Oct-14 A | |
| L09-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 23-Oct-14 A | 03-Nov-14 A | |

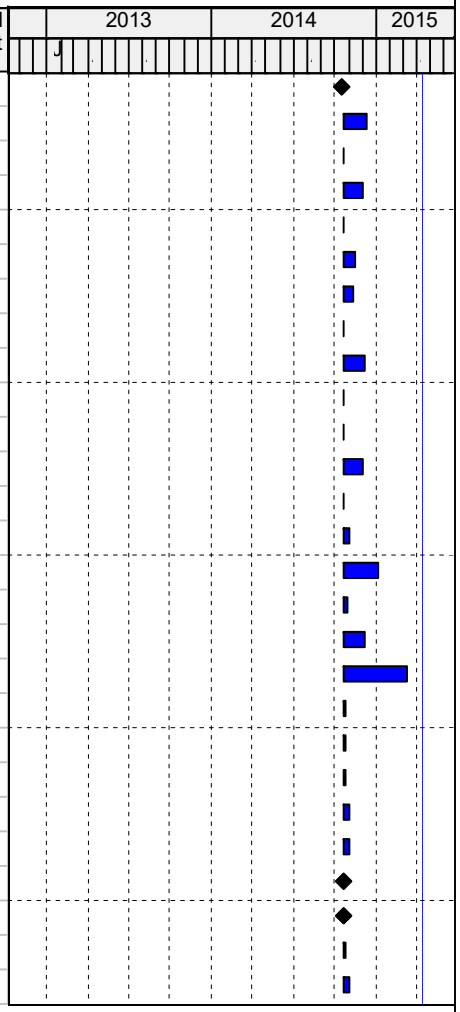



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| LL2-2078 | Generator - Install fuel fill control wiring | 2 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| I-2950 | Kitchen Hood Type 1 impact (COB correction notice, I | 1 | 0 | 23-Oct-14 A | 21-Dec-14 A | |
| RF-4050 | Roof at Manlift - Erect steel | 1 | 0 | 24-Oct-14 A | 24-Oct-14 A | |
| CO-7204 | Cx - Gas Service established | 0 | 0 | | 24-Oct-14 A | |
| I-5900 | Owner select color for Porte Cochere drive concrete | 20 | 0 | 24-Oct-14 A | 11-Mar-15 A | |
| L1BOH2-8102 | GWB Hang (Walls) | 4 | 0 | 27-Oct-14 A | 07-Nov-14 A | |
| L04-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 27-Oct-14 A | 12-Nov-14 A | |
| RF-4052 | Roof at Manlift - Framing/sheathing/air barrier (inspec | 4 | 0 | 27-Oct-14 A | 30-Oct-14 A | |
| LL2-2080 | Generator - Complete generator accessories (battery) | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| LL2-2082 | Generator - Cx fuel fill | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| L09-8130 | Install Door Hardware | 3 | 0 | 28-Oct-14 A | 04-Nov-14 A | |
| CO-7158 | Generator - Interim electrical inspection | 1 | 0 | 29-Oct-14 A | 29-Oct-14 A | |
| LL2-2070 | LL2 - Generator Room - Generator Ready for Startup | 0 | 0 | | 30-Oct-14 A | |
| LL2-2084 | Generator - Initial fuel fill | 1 | 0 | 30-Oct-14 A | 30-Oct-14 A | |
| CO-7200 | Cx - Penthouse Mechanical Installation Complete | 0 | 0 | | 30-Oct-14 A | |
| EL-6028 | Elev 6 - RFI-761: Response, pricing, complete work (r | 20 | 0 | 30-Oct-14 A | 27-Jan-15 A | |
| L03-8636 | Pool - Shotcrete | 1 | 0 | 31-Oct-14 A | 31-Oct-14 A | |
| RF-4054 | Roof at Manlift - Final mechanical installations | 4 | 0 | 31-Oct-14 A | 05-Nov-14 A | |
| RF-4056 | Roof at Manlift - Final electrical connections | 2 | 0 | 31-Oct-14 A | 05-Nov-14 A | |
| CO-7130 | Fire Alarm - Point-To-Point Wiring | 18 | 0 | 01-Nov-14 A | 06-Feb-15 A | |
| L03-8404 | GWB Hang/Tape Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 14-Nov-14 A | |
| L04-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 14-Nov-14 A | |
| L05-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 17-Nov-14 A | |
| L06-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 17-Nov-14 A | |
| L03-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L04-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |

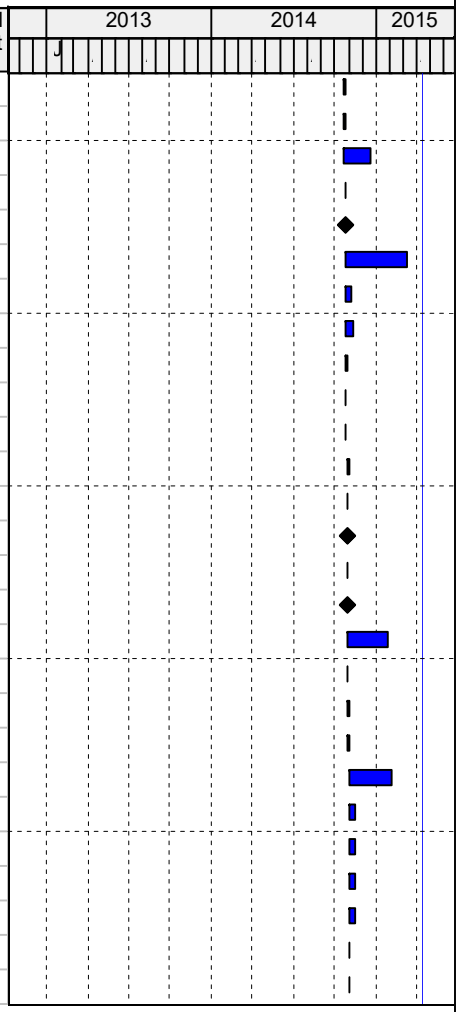



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L06-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L07-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L08-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L09-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L10-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L11-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L12-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L14-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L15-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L16-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L17-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L14-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 03-Nov-14 A | 06-Nov-14 A | |
| MPT-1024 | (A) Caulking - Elevation 41 (east elevation above poo | 7 | 0 | 03-Nov-14 A | 16-Dec-14 A | |
| CO-7206 | Cx - Purge/Prove Gas-Fed Equipment and Feeder Li | 7 | 0 | 03-Nov-14 A | 09-Nov-14 A | |
| I-5200 | Resolve MEP conflicts with ceiling grid (RFIs 783 & 8 | 8 | 0 | 03-Nov-14 A | 18-Mar-15 A | |
| I-5040 | RFI 776 - North Sidewalk-Entrance Conflicts | 1 | 0 | 03-Nov-14 A | 18-Dec-14 A | |
| L07-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 17-Nov-14 A | |
| L08-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L09-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L10-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L12-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L11-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 04-Nov-14 A | 15-Dec-14 A | |
| L11-8130 | Install Door Hardware | 3 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L10-8130 | Install Door Hardware | 3 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L11-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 18-Nov-14 A | |
| L12-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 19-Nov-14 A | |

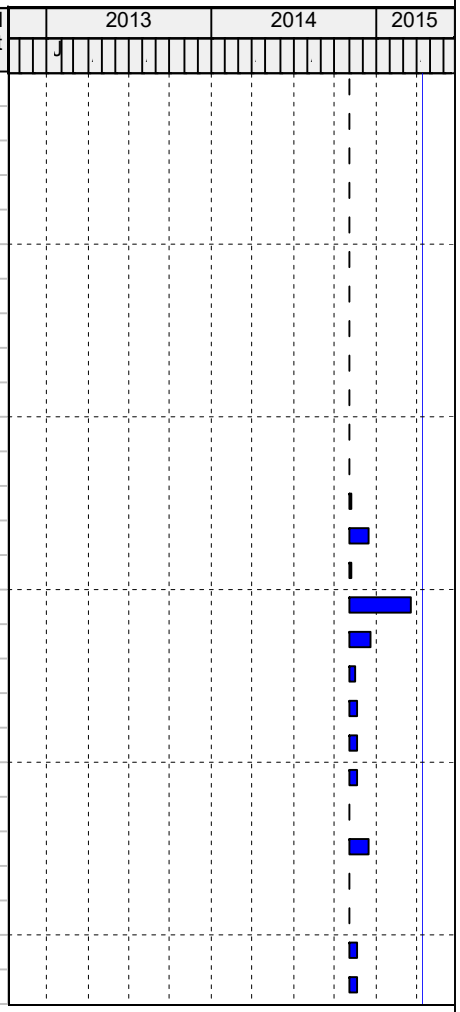



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 19-Nov-14 A | |
| MPP-1010 | Podium - Install East Elevation (Elev 5 & 7) | 7 | 0 | 05-Nov-14 A | 10-Dec-14 A | |
| CO-7162 | Generator - Load bank testing | 1 | 0 | 05-Nov-14 A | 05-Nov-14 A | |
| CO-7202 | Cx - Electrical Internal Bus & LL2-L17 Bus Duct Energ | 0 | 0 | | 05-Nov-14 A | |
| CO-7202a | Cx - Energize normal power distribution | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| I-5036 | RFI 717.1 - Porte Cochere Paving Details | 1 | 0 | 05-Nov-14 A | 26-Nov-14 A | |
| L15-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 19-Nov-14 A | |
| L16-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 20-Nov-14 A | |
| L17-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 20-Nov-14 A | |
| RF-4058 | Roof at Manlift - Install roofing | 2 | 0 | 06-Nov-14 A | 07-Nov-14 A | |
| CO-7164 | Generator - Final electrical inspection | 1 | 0 | 06-Nov-14 A | 06-Nov-14 A | |
| ASI59 | ASI No. 59 - Electrical One-Line Revisions | 0 | 0 | 06-Nov-14 A | | |
| I-5042 | RFI 796 - City Requested Added Scope | 1 | 0 | 06-Nov-14 A | 22-Dec-14 A | |
| I-5046 | RFI 803 - Site Light Bases Layout with Existing Sidew | 1 | 0 | 06-Nov-14 A | 14-Jan-15 A | |
| L15-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 07-Nov-14 A | 12-Nov-14 A | |
| L03-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L03-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L04-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L04-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L05-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L05-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L06-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L06-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L07-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L07-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L08-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L08-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |

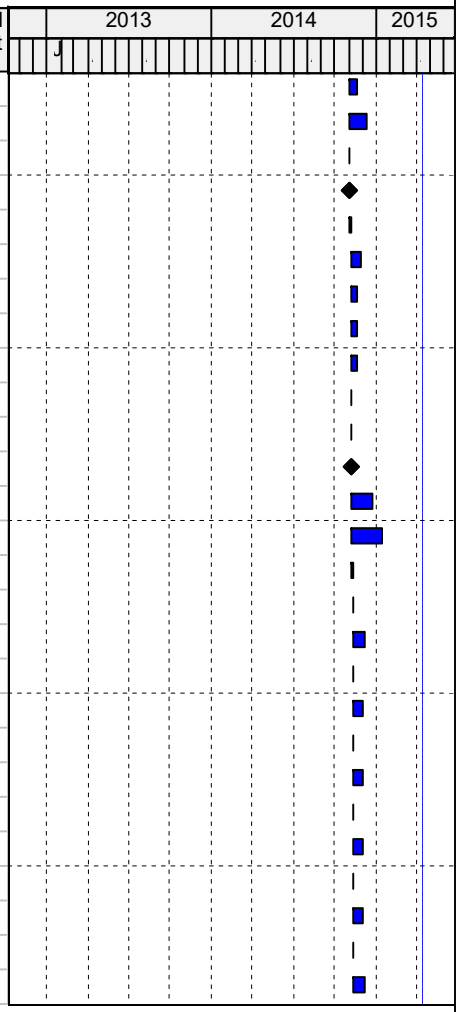



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L09-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L10-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L10-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L11-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L11-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L12-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L12-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L14-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L14-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L15-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L15-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L16-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L16-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L17-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L17-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L05-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| L06-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 10-Nov-14 A | 11-Nov-14 A | |
| MPT-1032 | Tower - Install sign backing NW (Elev 51,52) | 4 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L12-8130 | Install Door Hardware | 3 | 0 | 10-Nov-14 A | 12-Nov-14 A | |
| EL-1230 | Elev 1&2 - Complete hoistway ventilation | 13 | 0 | 10-Nov-14 A | 15-Dec-14 A | |
| EL-1232 | Elev 1&2 - Wire & startup AC split units | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-1234 | Elev 1&2 - Install EMR doors, hardware & labeling | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-3428 | Elev 3&4 - Complete hoistway ventilation | 13 | 0 | 10-Nov-14 A | 15-Dec-14 A | |
| EL-3430 | Elev 3&4 - Wire & startup AC split units | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-3432 | Elev 3&4 - Install EMR doors, hardware & labeling | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-6030 | Elev 6 - Complete fire-rated assemblies at hoistway, l | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |

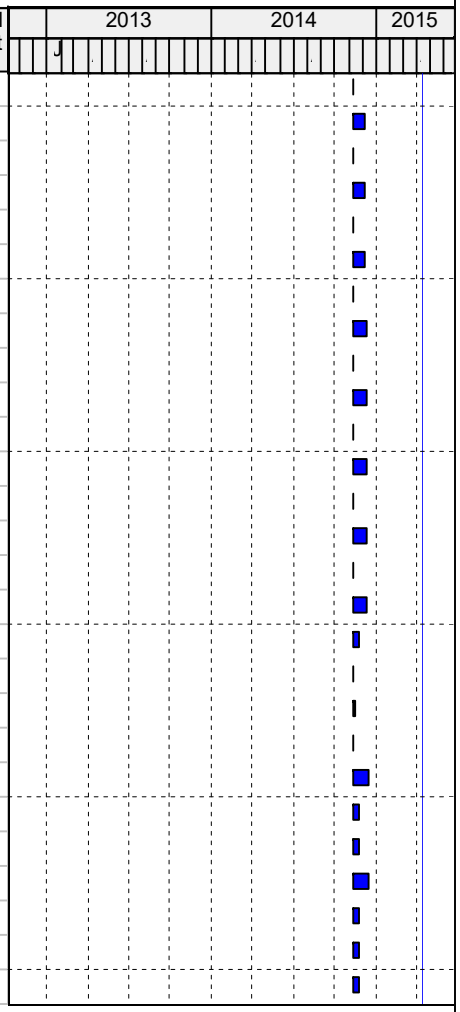



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 11-Nov-14 A | 12-Nov-14 A | |
| L16-8106 | Paint - Accent Walls | 2 | 0 | 11-Nov-14 A | 12-Nov-14 A | |
| L14-8130 | Install Door Hardware | 3 | 0 | 11-Nov-14 A | 13-Nov-14 A | |
| I-5044 | RFI 802 - Landscape Planter & Arch Detail Coordinati | 1 | 0 | 11-Nov-14 A | 18-Nov-14 A | |
| L03-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 12-Nov-14 A | 18-Nov-14 A | |
| SW-2104 | Zone 1 - Install lighting conduit at SE corner | 2 | 0 | 12-Nov-14 A | 14-Nov-14 A | |
| L16-8111 | Paint - Door Jambs | 2 | 0 | 12-Nov-14 A | 13-Nov-14 A | |
| EL-6010i | Elev 6 - Pit Slab Correction (form/pour/strip/clean) | 10 | 0 | 12-Nov-14 A | 26-Nov-14 A | |
| SW-2024 | Zone 4 - FRP Porte Cochere planter & bench | 6 | 0 | 12-Nov-14 A | 04-Dec-14 A | |
| L08-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| SW-2109 | Zone 1 - Install irrigation sleeves | 2 | 0 | 13-Nov-14 A | 14-Nov-14 A | |
| MPT-1026 | (C) Caulking - Elevation 47 (north elevation, east half | 10 | 0 | 13-Nov-14 A | 19-Dec-14 A | |
| L16-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| L15-8130 | Install Door Hardware | 3 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| ASI56 | ASI No. 56 - Interior Design Millwork and Finish Chan | 0 | 0 | 13-Nov-14 A | | |
| L04-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 14-Nov-14 A | 19-Nov-14 A | |
| SW-2203 | Zone 2 - Install irrigation sleeves | 2 | 0 | 14-Nov-14 A | 08-Jan-15 A | |
| L1B-8120 | Install operable partitions | 3 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| LL1-Z3-8340 | Install walk-in cooler/freezer (BY OTHERS) | 5 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| SW-2316 | Zone 3 - Demolish manlift shack and base | 5 | 0 | 17-Nov-14 A | 20-Nov-14 A | |
| I-1610 | Enclosure at manlift - Install exterior wall panels & ins | 5 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| L04-8140 | Install window sills | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| L03-8140x | Install window sills | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| L16-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| SW-2014 | Porte Cochere - Electrical rough-in | 5 | 0 | 17-Nov-14 A | 08-Dec-14 A | |
| I-5600 | Lower heat pump and install access panels (RFI 734) | 13 | 0 | 17-Nov-14 A | 09-Jan-15 A | |
| LL1-Z3-FCC26 | Program FACP & Stand-Up System | 20 | 0 | 17-Nov-14 A | 22-Jan-15 A | |

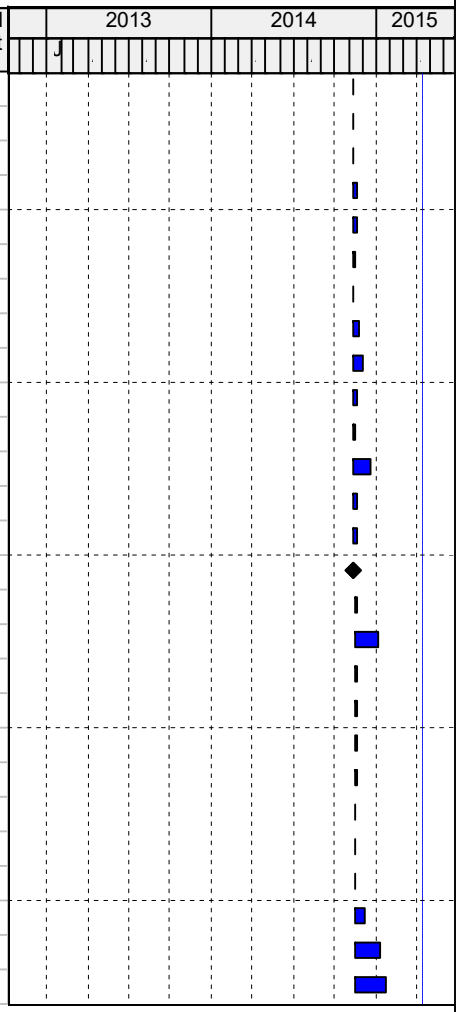



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8140 | Install window sills | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L05-8140 | Install window sills | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| I-5048 | RFI 805 - City Approved Public ROW Irrigation Lines M | 1 | 0 | 18-Nov-14 A | 05-Dec-14 A | |
| L05-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 19-Nov-14 A | 22-Dec-14 A | |
| L16-8130 | Install Door Hardware | 3 | 0 | 19-Nov-14 A | 02-Dec-14 A | |
| L08-8140 | Install window sills | 2 | 0 | 19-Nov-14 A | 19-Nov-14 A | |
| L07-8140 | Install window sills | 2 | 0 | 19-Nov-14 A | 19-Nov-14 A | |
| I-1616 | Enclosure at manlift - Patch/repair concrete shear wal | 3 | 0 | 19-Nov-14 A | 21-Nov-14 A | |
| ASI58 | ASI No. 58 - Level 1 Valet Phone and POS Locations | 0 | 0 | 19-Nov-14 A | | |
| ASI59ca | ASI No. 59 - Electrical One-Line Revisions (City Appro | 0 | 0 | 19-Nov-14 A | | |
| L10-8140 | Install window sills | 2 | 0 | 20-Nov-14 A | 20-Nov-14 A | |
| L09-8140 | Install window sills | 2 | 0 | 20-Nov-14 A | 20-Nov-14 A | |
| I-1622 | Manlift finishes - Install windows & caulk | 4 | 0 | 20-Nov-14 A | 03-Dec-14 A | |
| LL2-2060 | LL2 - Paint Laundry Room | 3 | 0 | 21-Nov-14 A | 24-Nov-14 A | |
| L03-8616 | L3 Pool - GWB above ceiling | 2 | 0 | 21-Nov-14 A | 22-Nov-14 A | |
| LL1-Z3-8342 | Final connections at walk-in cooler/freezer | 2 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L1K-8340 | Install walk-in cooler/freezer (BY OTHERS) | 2 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L10-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| L16-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| SW-2110 | Zone 1 - Adjust utilities structures | 5 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| SW-2214 | Zone 2 - Adjust utilities structures | 2 | 0 | 24-Nov-14 A | 25-Nov-14 A | |
| MPT-1030 | Tower - Install sign backing NE (Elev 44) | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| SW-2012 | Porte Cochere - Install cornice[DELETED SEE REV M | 8 | 0 | 24-Nov-14 A | 05-Dec-14 A | |
| L03-8650 | L3 Pool - Build scaffold at pool pit | 2 | 0 | 24-Nov-14 A | 25-Nov-14 A | |
| EL-6032 | Elev 6 - Install pit ladder | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| EL-6034 | Elev 6 - Install pit jack & hoistway pistons; connect hy | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| L06-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 25-Nov-14 A | 22-Dec-14 A | |

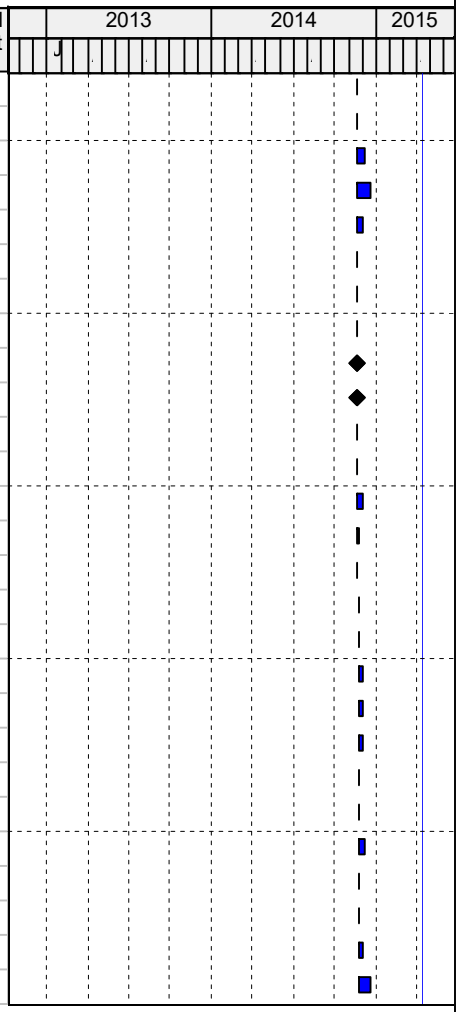



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8104a | L2 - Int Painting - South Half | 2 | 0 | 25-Nov-14 A | 26-Nov-14 A | |
| SW-2016 | Porte Cochere - Complete framing | 3 | 0 | 25-Nov-14 A | 01-Dec-14 A | |
| LL2-2096 | LL2 - Install FRP at Laundry Room | 8 | 0 | 25-Nov-14 A | 05-Dec-14 A | |
| I-1602 | Enclosure at manlift - Install shear wall clips and inspe | 4 | 0 | 26-Nov-14 A | 05-Dec-14 A | |
| L07-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| SW-2318 | Zone 3 - Install catch basin | 1 | 0 | 26-Nov-14 A | 26-Nov-14 A | |
| L03-8652 | L3 Pool - Frame ceiling | 4 | 0 | 26-Nov-14 A | 04-Dec-14 A | |
| I-5052 | RFI 819 - Flagpole Locations | 1 | 0 | 26-Nov-14 A | 30-Dec-14 A | |
| I-5050 | RFI 818 - 111th East Elevation Hardscape Vertical Dif | 1 | 0 | 26-Nov-14 A | 29-Dec-14 A | |
| L03-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L04-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L05-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L06-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L07-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L09-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L10-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L11-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L12-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L14-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L15-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L16-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L17-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 01-Dec-14 A | 04-Dec-14 A | |
| L02-6016a | L2 - Electrical Room Buildout | 5 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| L03-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L04-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |

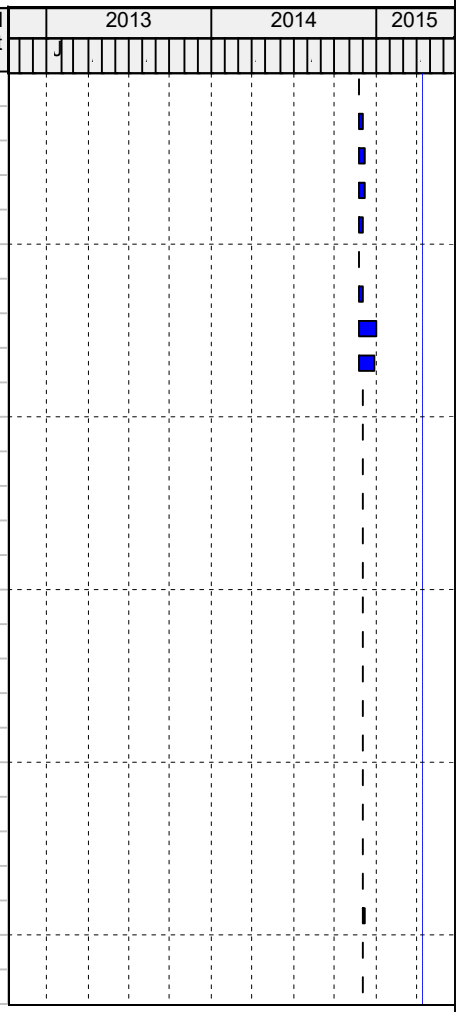



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L06-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L07-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L09-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L10-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L11-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L12-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L14-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L15-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L16-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L17-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| SW-2210 | Zone 2 - Fine grade for sidewalk | 5 | 0 | 01-Dec-14 A | 08-Jan-15 A | |
| RF-4040 | L2.5 Horseshoe - Install sheet metal capping[DELETI | 3 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| MPT-1042 | Enclosure at manlift - air barrier & inspect | 5 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| CO-7208 | Cx - Start-Up Pumps | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| CO-7210 | Cx - Start-Up VFD's | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| L17-8106 | Paint - Accent Walls | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| LL4-8116 | LL4 - Install ACT grid [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL3-8116 | LL3 - Install ACT grid [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| I-1630 | Manlift finishes - Framing, corridor ceilings & inspect | 4 | 0 | 01-Dec-14 A | 09-Dec-14 A | |
| EL-6036 | Elev 6 - Install shunt trip breaker | 5 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| L17-8111 | Paint - Door Jambs | 2 | 0 | 02-Dec-14 A | 03-Dec-14 A | |
| SW-2018 | Porte Cochere - GWB hang/tape | 3 | 0 | 02-Dec-14 A | 09-Dec-14 A | |
| L03-8654 | L3 Pool - HVAC drops at ceiling & inspect | 3 | 0 | 02-Dec-14 A | 05-Dec-14 A | |
| L11-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 03-Dec-14 A | 08-Dec-14 A | |
| SW-2308 | Zone 3 - Install site lighting | 5 | 0 | 03-Dec-14 A | 04-Dec-14 A | |

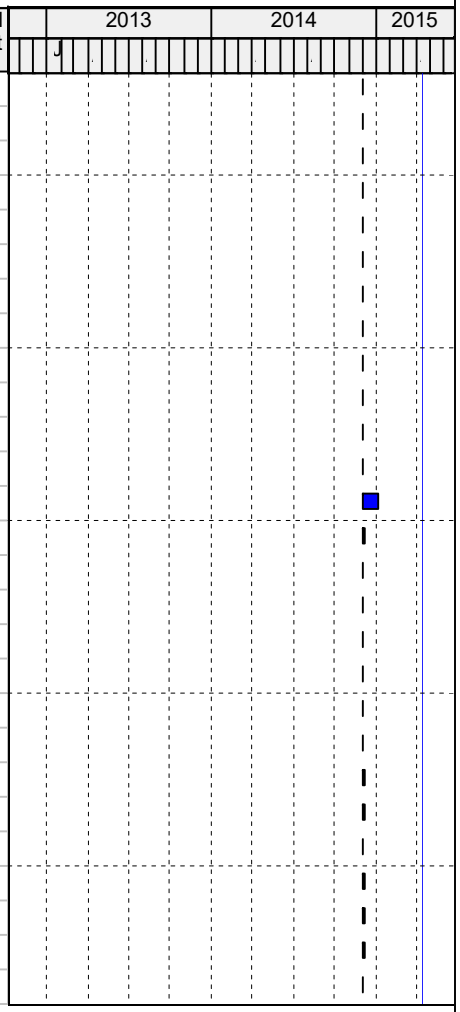



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 03-Dec-14 A | 15-Dec-14 A | |
| I-1632 | Manlift finishes - Electrical rough-in & inspect | 2 | 0 | 03-Dec-14 A | 10-Dec-14 A | |
| SW-2028 | Zone 4 - Scan Porte Cochere deck | 2 | 0 | 04-Dec-14 A | 05-Dec-14 A | |
| I-1624 | Manlift finishes - Install batt insulation & inspect | 2 | 0 | 04-Dec-14 A | 04-Dec-14 A | |
| I-1626 | Manlift finishes - Shim window openings | 2 | 0 | 04-Dec-14 A | 05-Dec-14 A | |
| I-1628 | Manlift finishes - Install vapor barrier & inspect | 2 | 0 | 04-Dec-14 A | 08-Dec-14 A | |
| I-5054 | RFI 832.1 - South Elevation Emergency Exit with Side | 1 | 0 | 04-Dec-14 A | 18-Dec-14 A | |
| I-1608 | Tower - Install N/S Wing, S. End at manlift (Elev 32) [I | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1012 | Tower - Install N/S Wing, S. End E. Side Concrete (El | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| PC-4012 | Porte Cochere - Install sheet metal capping[DELETEI | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4046 | Tower Roof - Install sheet metal capping[DELETED S | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4060 | Roof at Manlift - Install corrugated metal panels[DELE | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4062 | Roof at Manlift - Install sheet metal capping[DELETEI | 2 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4064 | Pool Green Roof - Install sheet metal capping[DELET | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1040 | Tower - Install N/S Wing, S, End (Elev 30)[DELETED | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1044 | Enclosure at manlift - Install sign backing south[DELE | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1612 | Enclosure at manlift - Caulking[DELETED SEE REV M | 8 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1614 | Enclosure at manlift - Install rigid insulation at shear w | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1618 | Enclosure at manlift - Install framing at shear wall[DEI | 5 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1620 | Enclosure at manlift - Install hat channel over framing | 5 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| L03-8656 | L3 Pool - Electrical rough-in at ceiling & inspect | 3 | 0 | 05-Dec-14 A | 19-Dec-14 A | |
| I-5058 | RFI 834 - NE Retaining Wall Design Clarifications | 1 | 0 | 05-Dec-14 A | 23-Dec-14 A | |
| I-5062 | RFI 835 - NW Planter Wall Drainage | 1 | 0 | 05-Dec-14 A | 10-Dec-14 A | |
| L1K-8344 | Set kitchen hoods | 8 | 0 | 06-Dec-14 A | 21-Dec-14 A | |
| L12-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L03-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |
| L04-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |

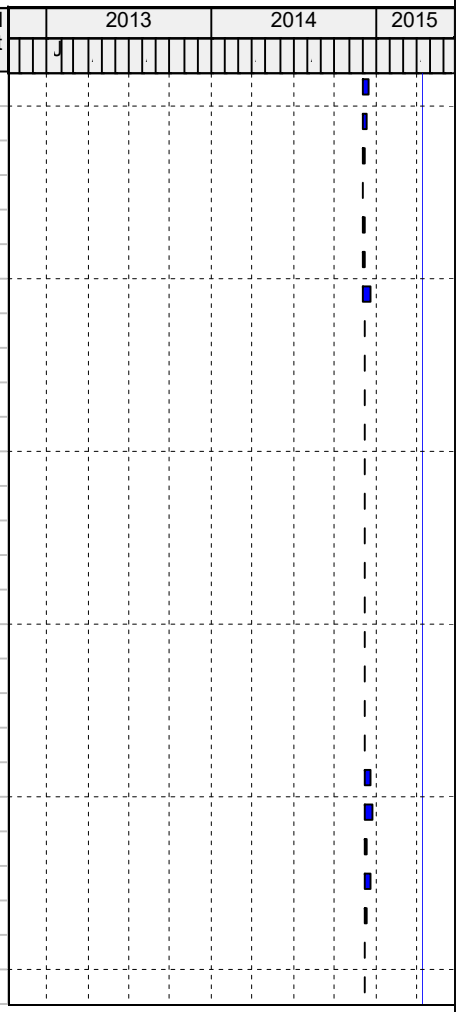



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |
| SW-2312 | Zone 3 - Fine grade for sidewalk | 3 | 0 | 08-Dec-14 A | 08-Jan-15 A | |
| RF-4042 | Pool Roof - Install metal coping at high roof | 2 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L17-8130 | Install Door Hardware | 3 | 0 | 08-Dec-14 A | 11-Dec-14 A | |
| L09-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L03-8658 | L3 Pool - Fire sprinkler drops at ceiling & inspect | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| LL2-8140 | LL2 - Install vinyl wall coverings | 2 | 0 | 08-Dec-14 A | 24-Dec-14 A | |
| L04-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L05-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L07-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L08-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L14-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L15-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 09-Dec-14 A | 12-Dec-14 A | |
| L03-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L07-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L08-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L04-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L05-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L07-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L08-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |

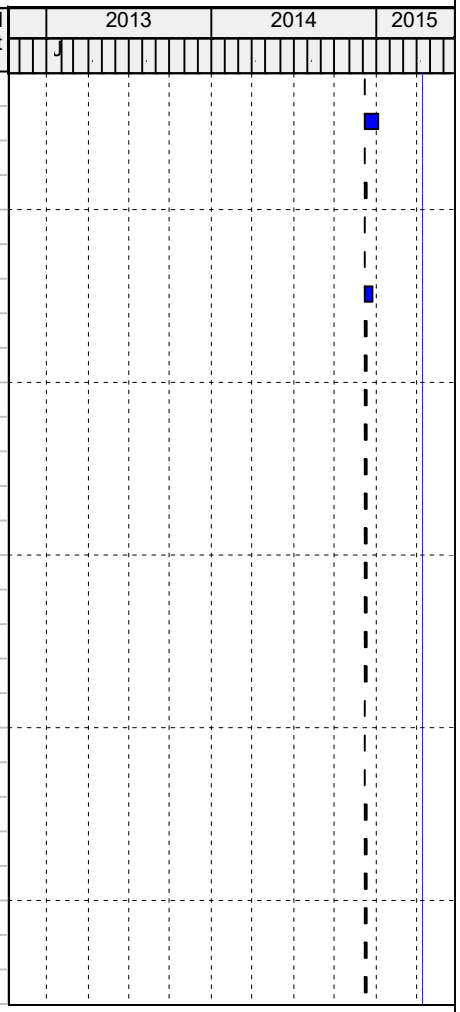



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| RF-4072 | Pool Roof - Install metal coping | 3 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L17-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 09-Dec-14 A | 12-Dec-14 A | |
| L07-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 09-Dec-14 A | 29-Dec-14 A | |
| L06-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 09-Dec-14 A | 24-Dec-14 A | |
| I-1604 | Manlift finishes - GWB, hang walls | 2 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L07-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L08-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 16-Dec-14 A | |
| L11-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L12-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L14-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L15-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L16-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L17-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| LL2E-8340 | LL2 - Install walk-in cooler/freezer (BY OTHERS) | 5 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L10-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 10-Dec-14 A | 17-Dec-14 A | |
| L09-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L10-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L11-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L11-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L12-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L14-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L15-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L16-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L17-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L08-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 10-Dec-14 A | 29-Dec-14 A | |
| I-1634 | Manlift finishes - GWB, hang ceilings | 2 | 0 | 10-Dec-14 A | 16-Dec-14 A | |

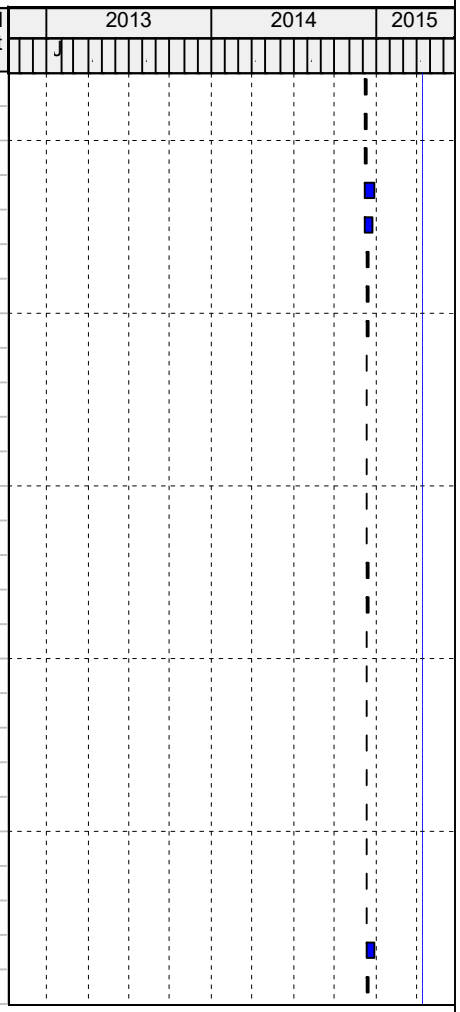



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L14-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L15-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L03-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L04-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| MPT-1034 | (A) Elevation 52 (west elevation, north end, L3-L18) | 4 | 0 | 11-Dec-14 A | 16-Dec-14 A | |
| MPT-1036 | (B) Elevation 45/46 (north elevation, east end, L3-L1 | 5 | 0 | 11-Dec-14 A | 19-Dec-14 A | |
| L16-7030 | Paint | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L17-7030 | Paint | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L05-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L06-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| MPT-1066 | Tower Sign, East (El. 32) - Install backing | 3 | 0 | 12-Dec-14 A | 22-Dec-14 A | |
| MPT-1076 | (B) Caulking - Elevation 51 (north elevation, west half | 10 | 0 | 12-Dec-14 A | 19-Dec-14 A | |
| L04-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L04-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L07-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L08-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L09-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L14-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L15-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L17-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 16-Dec-14 A | |
| L04-7042 | Install Tile Flooring (x41) | 2 | 0 | 15-Dec-14 A | 24-Dec-14 A | |
| L05-7042 | Install Tile Flooring (x41) | 2 | 0 | 15-Dec-14 A | 24-Dec-14 A | |

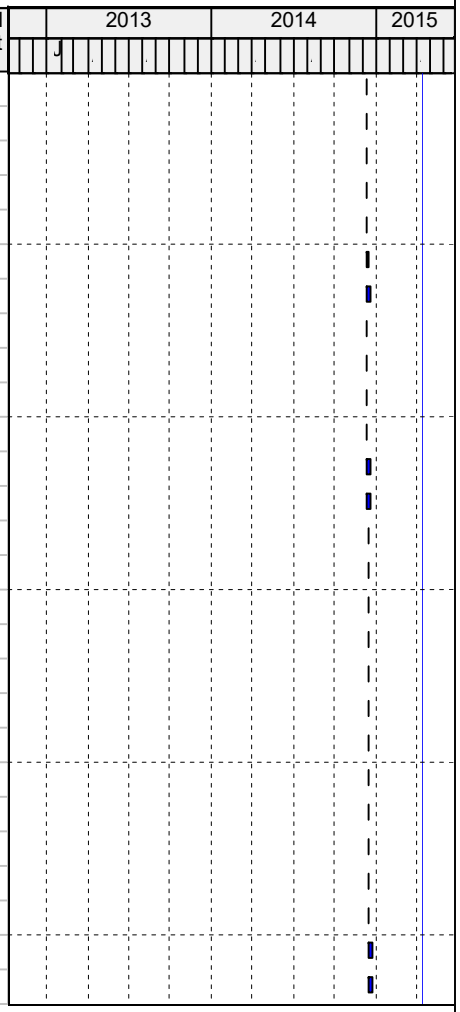



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8102a | LL4 - GWB Tape/Finish | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| LL3-8102a | LL3 - GWB Tape/Finish | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| L03-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L04-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L07-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L08-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L09-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L10-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| CO-7126 | Fire pump test pre-planning complete (see checklist) | 0 | 0 | | 15-Dec-14 A | |
| LL1-Z3-6034 | COB Correction - Add ceiling access panels in Food F | 10 | 0 | 15-Dec-14 A | 26-Jan-15 A | |
| L03-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| L05-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L09-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L10-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L10-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L11-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L11-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L14-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L15-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L16-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L17-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| LL2E-8342 | LL2 - Final connections at walk-in cooler/freezer | 5 | 0 | 16-Dec-14 A | 05-Jan-15 A | |
| L11-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 16-Dec-14 A | 18-Dec-14 A | |

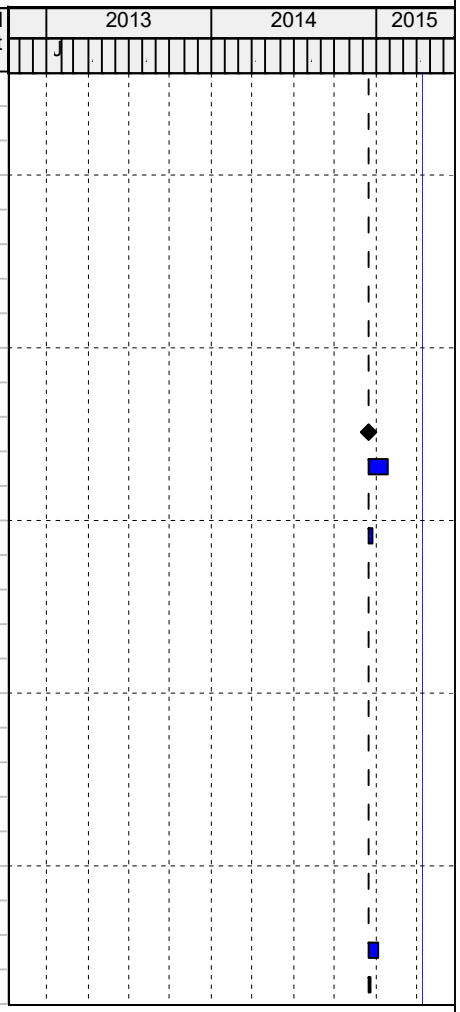



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8201 | Corridors - Install ACT Grid | 2 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L06-7042 | Install Tile Flooring (x41) | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L07-7042 | Install Tile Flooring (x41) | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| LL1-Z2-8102a | GWB Hang (Ceilings) & Inspection | 3 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L11-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L14-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L15-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L16-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L17-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| CO-7128 | Run fire pump test | 2 | 0 | 16-Dec-14 A | 17-Dec-14 A | |
| L09-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 16-Dec-14 A | 30-Dec-14 A | |
| SW-2026 | Zone 4 - FRP NW planter | 5 | 0 | 16-Dec-14 A | 05-Jan-15 A | |
| I-5370 | (S) Resolve south tower sign backing (RFI 844) | 5 | 0 | 16-Dec-14 A | 09-Jan-15 A | |
| L03-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 22-Dec-14 A | |
| L04-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 23-Dec-14 A | |
| L06-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 29-Dec-14 A | |
| L07-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 30-Dec-14 A | |
| L08-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 31-Dec-14 A | |
| L09-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 05-Jan-15 A | |
| L14-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L15-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L16-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L17-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L08-7042 | Install Tile Flooring (x41) | 2 | 0 | 17-Dec-14 A | 24-Dec-14 A | |
| L09-7042 | Install Tile Flooring (x41) | 2 | 0 | 17-Dec-14 A | 24-Dec-14 A | |
| L04-7136 | Install Door and Hardware | 1 | 0 | 17-Dec-14 A | 17-Dec-14 A | |

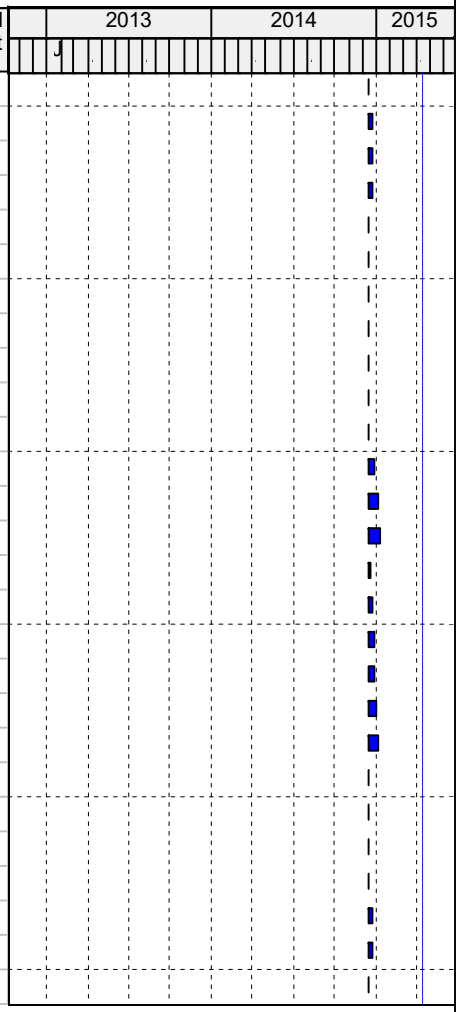



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 17-Dec-14 A | 29-Dec-14 A | |
| MPT-1046 | (A) Elevation 26/27/53 (west elevation, south of 52, L | 3 | 0 | 17-Dec-14 A | 18-Dec-14 A | |
| MPT-1057 | (S) Elevation 32 framing (south elevation, east of mai | 5 | 0 | 17-Dec-14 A | 19-Jan-15 A | |
| MPT-1080 | (A) Caulking - Elevation 44 (east elevation above poo | 8 | 0 | 17-Dec-14 A | 22-Dec-14 A | |
| LL1-Z2-8108 | Framing, ceiling clouds (incl. inspection) | 5 | 0 | 17-Dec-14 A | 22-Jan-15 A | |
| MPP-1006 | (C) Install Level 3 cornice metal (north, west & south) | 6 | 0 | 18-Dec-14 A | 30-Jan-15 A | |
| L10-7042 | Install Tile Flooring (x41) | 2 | 0 | 18-Dec-14 A | 24-Dec-14 A | |
| L11-7042 | Install Tile Flooring (x41) | 2 | 0 | 18-Dec-14 A | 24-Dec-14 A | |
| L12-7042 | Install Tile Flooring (x41) | 2 | 0 | 19-Dec-14 A | 24-Dec-14 A | |
| L14-7042 | Install Tile Flooring (x41) | 2 | 0 | 19-Dec-14 A | 24-Dec-14 A | |
| MPT-1048 | (B) Elevation 37 (penthouse east) | 3 | 0 | 19-Dec-14 A | 20-Dec-14 A | |
| I-5000 | Resolve RFI's and site work changes (new drawings) · | 10 | 0 | 19-Dec-14 A | 02-Mar-15 A | |
| I-5002 | Resolve RFI's and site work changes (new drawings) · | 20 | 0 | 19-Dec-14 A | 09-Feb-15 A | |
| I-5003 | Resolve RFI's and site work changes (new drawings) · | 10 | 0 | 19-Dec-14 A | 02-Mar-15 A | |
| I-5004 | Resolve RFI's and site work changes (new drawings) · | 1 | 0 | 19-Dec-14 A | 16-Jan-15 A | |
| I-5064 | RFI 848 - Lighting at Flagpole Locations | 1 | 0 | 19-Dec-14 A | 14-Jan-15 A | |
| L03-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 22-Dec-14 A | 22-Dec-14 A | |
| L07-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L17-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| CO-7212 | Cx - Start-Up Boilers | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L17-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L08-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L07-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L06-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L05-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L04-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 22-Dec-14 A | |
| I-1636 | Manlift finishes - GWB, tape & finish | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |

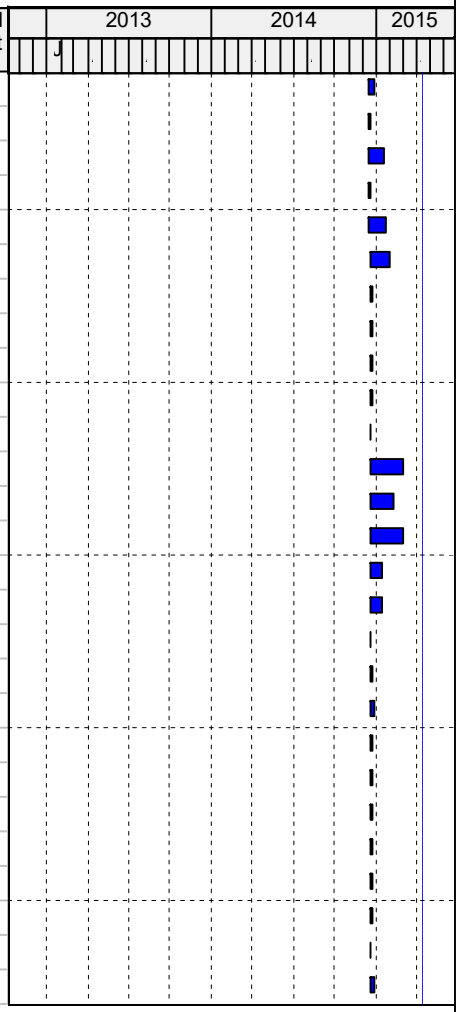



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6038 | Elev 6 - Rough-in call boxes & lanterns | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| EL-6052 | Elev 6 - Complete hoistway ventilation | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| MPT-1078 | (C) Caulking - Elevation 37/38/39 (penthouse) | 4 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| MPT-1086 | (A) Caulking - Elevation 45/46 (north elevation, east e | 7 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| MPT-1088 | (B) Caulking - Elevation 52/53/26/27 (west elevation, | 11 | 0 | 22-Dec-14 A | 02-Jan-15 A | |
| MPP-1044 | Caulking - Elevation 9/10/11/12/13 (upper ballroom) | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| MPP-1046 | Caulking - Elevation 5/6 (east elevation, south end) | 8 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| I-5068 | RFI 857 - South Elevation Landscape & Irrigation Re | 1 | 0 | 22-Dec-14 A | 07-Jan-15 A | |
| I-5070 | RFI 858 - North Elevation Landscape & Irrigation Req | 1 | 0 | 22-Dec-14 A | 07-Jan-15 A | |
| I-5072 | RFI 859 - Additional Curbs at Openings (see RFI 776) | 1 | 0 | 22-Dec-14 A | 07-Jan-15 A | |
| L03-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L03-7032 | Install VCT Flooring (x42) | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L08-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L10-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L09-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| ASI62 | ASI No. 62 - Civil Site Grading Revisions | 0 | 0 | 23-Dec-14 A | | |
| I-5074 | RFI 860 - SE Corner Hardscape Additional Clarificatio | 1 | 0 | 23-Dec-14 A | 07-Jan-15 A | |
| L09-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 24-Dec-14 A | 29-Dec-14 A | |
| L03-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 31-Dec-14 A | |
| L15-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L16-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L17-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L04-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L05-7136 | Install Door and Hardware | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L10-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L17-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| LL1-Z3-8202 | Install FRP wall coverings | 4 | 0 | 29-Dec-14 A | 06-Jan-15 A | |

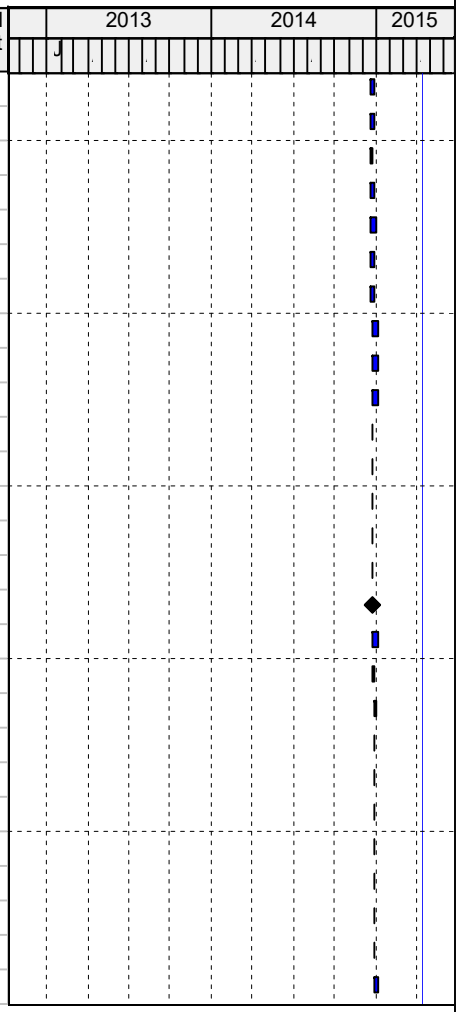



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L05-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L06-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L07-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L08-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L09-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L10-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL2-8130 | LL2 - Install ceiling grid | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| I-5300 | Heat Pump Revision - demo existing ceiling framing | 2 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L12-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 30-Dec-14 A | 05-Jan-15 A | |
| L06-7136 | Install Door and Hardware | 1 | 0 | 30-Dec-14 A | 30-Dec-14 A | |
| L11-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 30-Dec-14 A | 31-Dec-14 A | |
| I-5302 | Heat Pump Revision - rework MEP at celing | 5 | 0 | 30-Dec-14 A | 12-Jan-15 A | |
| I-1606 | Manlift finishes - Prime & paint | 4 | 0 | 31-Dec-14 A | 06-Jan-15 A | |
| L07-7136 | Install Door and Hardware | 1 | 0 | 31-Dec-14 A | 31-Dec-14 A | |
| L12-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 31-Dec-14 A | 05-Jan-15 A | |
| CO-7214 | Cx - Flush & Fill HVAC Hydronics Systems | 5 | 0 | 02-Jan-15 A | 05-Jan-15 A | |
| MPP-1032 | (C) Elevation 23/24/25 (Porte Cochere north, below c | 5 | 0 | 02-Jan-15 A | 19-Jan-15 A | |
| L1BOH2-8215 | GWB tape & finish walls & ceilings | 7 | 0 | 05-Jan-15 A | 02-Mar-15 A | |
| L10-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| L11-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 13-Jan-15 A | |
| L12-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 13-Jan-15 A | |
| L14-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| L16-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L04-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L05-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L06-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |

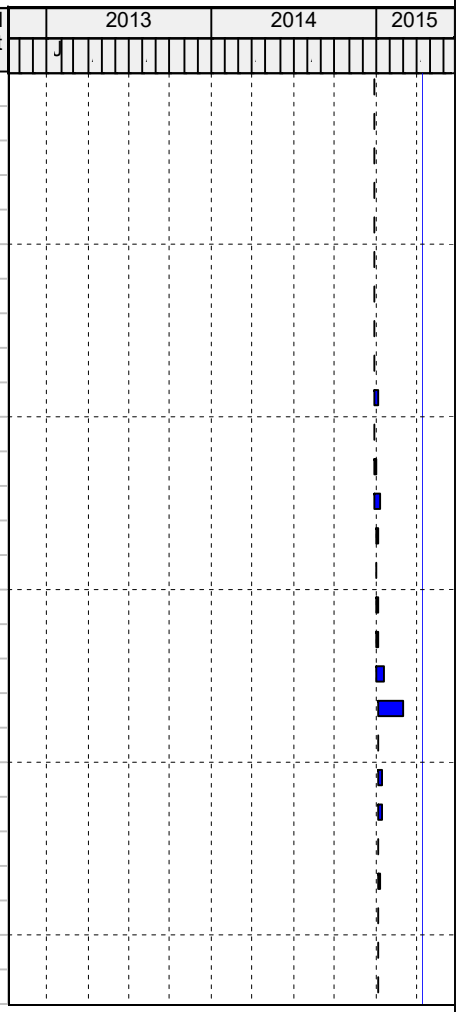



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| L06-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L07-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L08-7136 | Install Door and Hardware | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L08-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L09-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L10-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L14-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| SW-2314 | Zone 3 - FRP sidewalk | 5 | 0 | 05-Jan-15 A | 16-Feb-15 A | |
| L10-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 05-Jan-15 A | 27-Jan-15 A | |
| CO-7240 | Cx - Heat Pump Start-Up - Levels 3 & 4 | 5 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| SW-2220 | Zone 2 - FRP curb/gutter at NW corner | 4 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| MPT-1054 | Complete Elevation 30 (south elevation, west of man | 5 | 0 | 05-Jan-15 A | 18-Mar-15 A | |
| MPP-1028 | (C) Tapered pilasters, west | 3 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| MPP-1030 | (C) Tapered pilasters, east | 3 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| LL2-8142 | HVAC drops/trim to grid | 3 | 0 | 05-Jan-15 A | 19-Jan-15 A | |
| L1L-8216 | Complete electrical/fire alarm drops @ ceilings | 5 | 0 | 05-Jan-15 A | 08-Jan-15 A | |
| L1BOH2-8217 | GWB hang ceilings and at heat pumps | 10 | 0 | 05-Jan-15 A | 29-Jan-15 A | |
| L1L-8222 | Complete HVAC drops @ ceilings | 5 | 0 | 05-Jan-15 A | 23-Jan-15 A | |
| L1L-8224 | Complete fire sprinkler drops @ ceilings | 5 | 0 | 05-Jan-15 A | 08-Jan-15 A | |
| L1L-8254 | Complete electrical rough-in at walls | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| I-5350 | Fabricate & install new hydraulic ram | 30 | 0 | 05-Jan-15 A | 29-Jan-15 A | |
| SW-2226 | Zone 2 - Procure light poles and replacement luminai | 40 | 40 | 05-Jan-15 A | 08-Jun-15 | 0 |
| LL1-8120 | Complete GWB tape & finish in corridors | 7 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| L1K-8108 | Complete kitchen hood installation and fire blanket w | 10 | 0 | 05-Jan-15 A | 05-Feb-15 A | |
| L1K-8110 | Complete MEP rough-in above ceiling | 10 | 0 | 05-Jan-15 A | 05-Feb-15 A | |
| L1B-8122 | Framing, complete ceiling at corridors | 5 | 0 | 05-Jan-15 A | 13-Jan-15 A | |

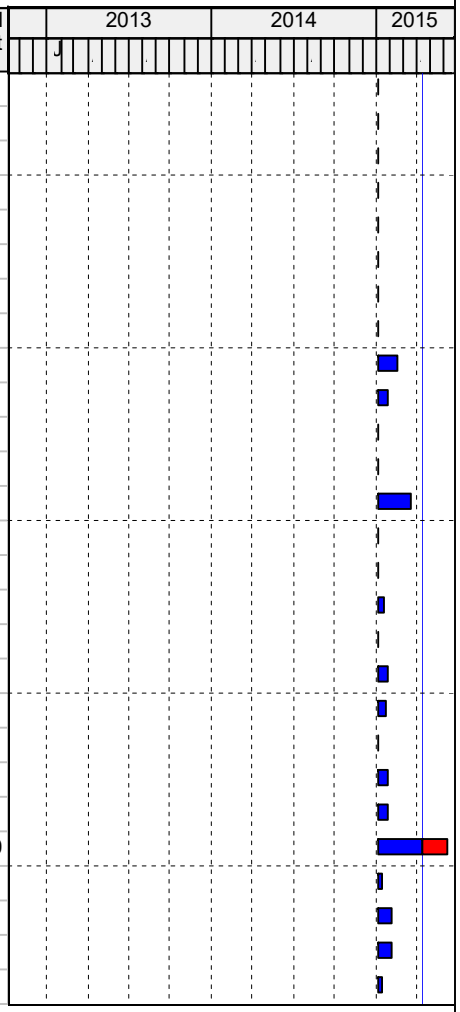



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-5102 | Bar lighting layout - resolve conflicts (RFI) | 7 | 0 | 05-Jan-15 A | 19-Jan-15 A | |
| I-5110 | Bar radius ceiling - resolve framing issues | 5 | 0 | 05-Jan-15 A | 14-Jan-15 A | |
| I-5120 | Dining feature wall - resolve design issues | 7 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| L02-8178 | Complete heat pump enclosures | 5 | 0 | 05-Jan-15 A | 12-Jan-15 A | |
| I-5850 | Owner provide revised lighting layout | 10 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| I-5130 | Bar plumbing relocation - resolve conflicts | 25 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| I-5140 | Damper at BPF #8 - resolve conflicts | 30 | 0 | 05-Jan-15 A | 29-Jan-15 A | |
| I-5150 | Sprinkler pipe furring - resolve conflicts | 15 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| I-5160 | ASI 63 electrical revisions - resolve conflicts | 10 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| L15-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 06-Jan-15 A | 07-Jan-15 A | |
| L07-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L08-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L09-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L10-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L09-7136 | Install Door and Hardware | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L10-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L11-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L12-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L15-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 06-Jan-15 A | 07-Jan-15 A | |
| L11-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 06-Jan-15 A | 12-Jan-15 A | |
| L03-8660 | GWB hang ceilings at Pool | 3 | 0 | 06-Jan-15 A | 04-Feb-15 A | |
| L1K-6011 | Complete HVAC RI @ ceilings | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L1K-6013 | Complete electrical rough-in @ ceilings & inspection | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L1K-6015 | Complete fire sprinkler RI @ ceilings | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L12-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L14-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L15-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |

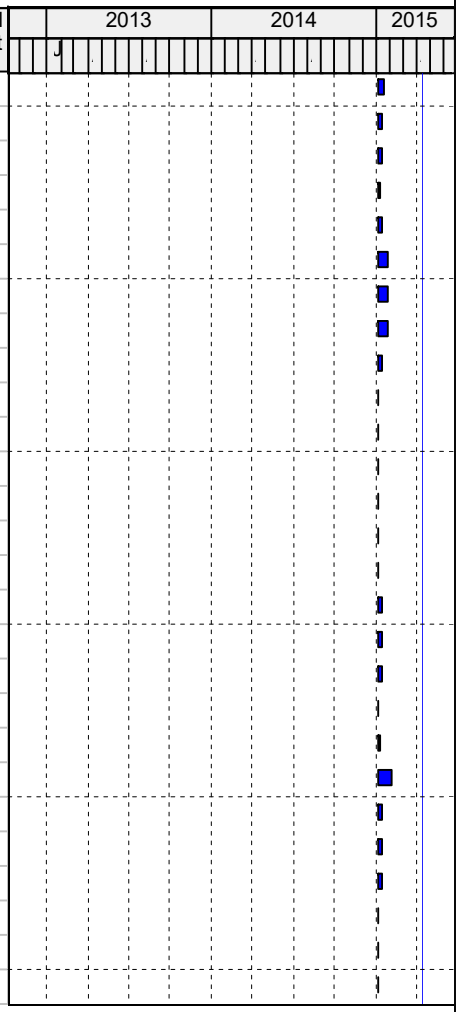



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L15-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 07-Jan-15 A | 20-Jan-15 A | |
| L12-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 07-Jan-15 A | 13-Jan-15 A | |
| CO-7242 | Cx - Heat Pump Start-Up - Levels 5 & 6 | 5 | 0 | 07-Jan-15 A | 09-Jan-15 A | |
| CO-7252 | Cx - Start-Up - FSD & SD Operation Verification | 10 | 0 | 07-Jan-15 A | 22-Jan-15 A | |
| MPP-1026 | Complete Elevation 7/8 (east elevation) | 5 | 0 | 07-Jan-15 A | 16-Feb-15 A | |
| ASI61 | ASI No. 61 - VHP-1 Ductwork Change at Elevator 5 L | 0 | 0 | 07-Jan-15 A | | |
| I-5056 | RFI 832.1 - South Elevation Emergency Exit with Sid | 1 | 0 | 07-Jan-15 A | 14-Jan-15 A | |
| LL1-6014Ib2 | L1 bar redesign - GWB hang, tape, finish (including ir | 12 | 0 | 08-Jan-15 A | 30-Jan-15 A | |
| SW-2310 | Zone 3 - Install irrigation sleeves | 2 | 0 | 08-Jan-15 A | 08-Jan-15 A | |
| I-1638 | Manlift finishes - ceiling grid | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| L03-8662 | GWB tape & finish walls & ceilings at Pool | 7 | 0 | 08-Jan-15 A | 25-Feb-15 A | |
| MPT-1072 | Tower Sign, West (El, 52) | 5 | 1 | 08-Jan-15 A | 13-Apr-15 | 12 |
| L1L-8220 | Complete fire sprinkler RI @ ceilings | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| L1L-8270 | Complete HVAC RI @ ceilings | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| SW-2224 | Zone 2 - Adjust Comcast vault lids | 2 | 0 | 08-Jan-15 A | 08-Jan-15 A | |
| I-1212 | Resolve stud/duct conflict at east wall | 5 | 0 | 08-Jan-15 A | 14-Jan-15 A | |
| L04-8218 | Install base at corridors (& approve mockup) | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| GB410-100 | Complete GWB - Levels 4-10 | 5 | 0 | 08-Jan-15 A | 14-Jan-15 A | |
| LL1-6014Ib4 | L1 bar redesign - complete reframing | 5 | 0 | 08-Jan-15 A | 15-Jan-15 A | |
| I-5306 | Heat Pump Revision - complete reframing | 5 | 0 | 08-Jan-15 A | 19-Jan-15 A | |
| ASI63 | ASI No. 63 - Mech (Rev. 20), Plumbing (Rev. 18) and | 0 | 0 | 09-Jan-15 A | | |
| L15-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L16-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8121 | Install Bathroom "Barn Doors" | 3 | 0 | 12-Jan-15 A | 26-Mar-15 A | |
| L04-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |

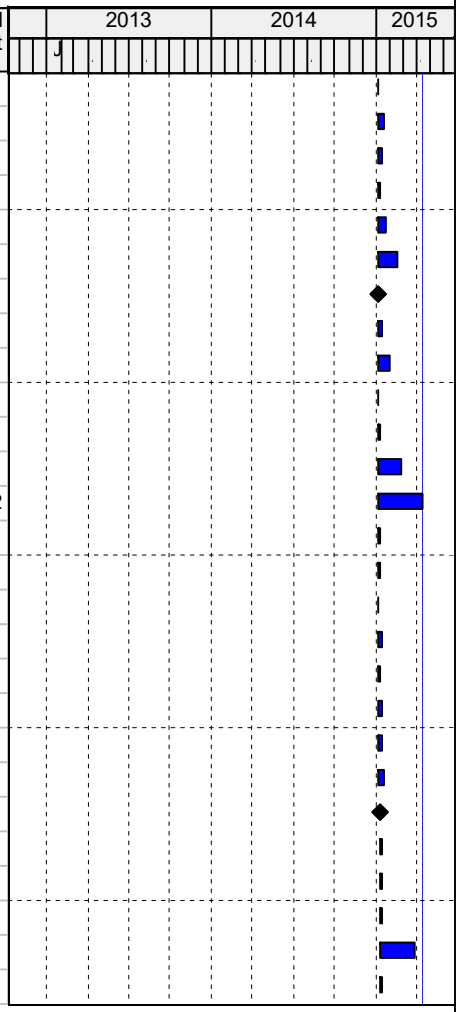



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L06-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L07-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L08-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L09-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L10-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L11-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L12-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L14-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L15-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L11-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L14-7136 | Install doors & hardware | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L14-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L15-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L15-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L14-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L11-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L03-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 12-Jan-15 A | 19-Jan-15 A | |
| CO-7244 | Cx - Heat Pump Start-Up - Levels 7 & 8 | 5 | 0 | 12-Jan-15 A | 14-Jan-15 A | |
| MPT-1068 | Tower Sign, North (El. 51) | 5 | 0 | 12-Jan-15 A | 10-Mar-15 A | |
| L03-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L11-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L14-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L15-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |

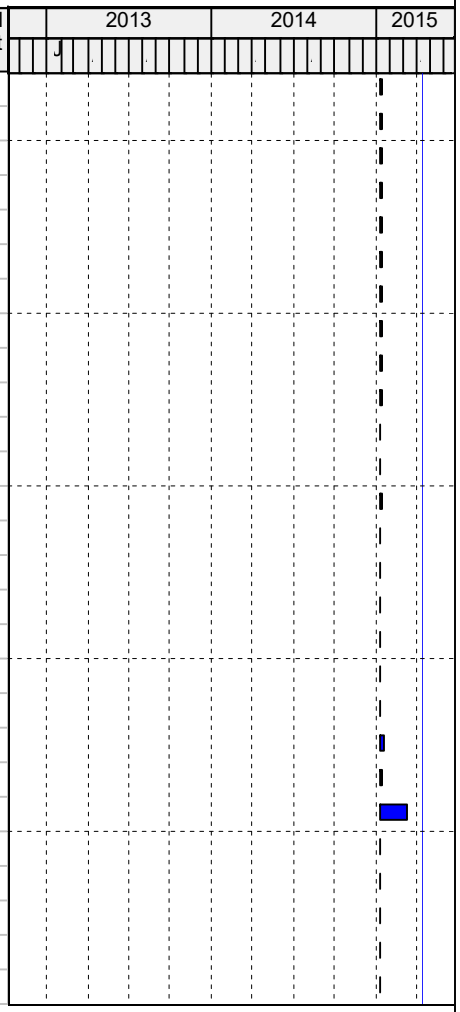



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8144 | GWB hang at Locker Rooms | 2 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| SW-2326 | Zone 3 - Install j-boxes | 3 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| I-5800 | Mechanical correction notice - interference with light t | 10 | 0 | 12-Jan-15 A | 13-Feb-15 A | |
| I-5602 | Frame FCC ceiling | 2 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| CO-7166 | Replace exhaust fitting | 10 | 0 | 12-Jan-15 A | 28-Jan-15 A | |
| MPP-1034 | Deliver Elevation 48 corner panels | 25 | 0 | 12-Jan-15 A | 27-Feb-15 A | |
| MPP-1042 | Deliver Elevation 32 corner panels | 25 | 0 | 12-Jan-15 A | 02-Feb-15 A | |
| MPP-1066 | Deliver Elevation 33/34 corner panels | 25 | 0 | 12-Jan-15 A | 27-Feb-15 A | |
| MPP-1068 | Deliver Elevation 32 spandrel panel head/sill flashings | 25 | 0 | 12-Jan-15 A | 13-Feb-15 A | |
| MPP-1070 | Deliver Elevation 44 spandrel panel head/sill flashings | 25 | 0 | 12-Jan-15 A | 13-Feb-15 A | |
| MPP-1072 | Deliver remaining Elevation 4 panels | 25 | 0 | 12-Jan-15 A | 06-Feb-15 A | |
| MPP-1074 | Deliver remaining Elevation 7 panels | 25 | 0 | 12-Jan-15 A | 06-Feb-15 A | |
| MPP-1076 | Deliver Pool cornice panels | 25 | 0 | 12-Jan-15 A | 23-Mar-15 A | |
| ASI64 | ASI No. 64 - Updated Public Space Carpet Specificat | 0 | 0 | 12-Jan-15 A | | |
| L15-7136 | Install doors & hardware | 1 | 0 | 13-Jan-15 A | 16-Feb-15 A | |
| L03-8664 | Paint, prime & first coat finish at Pool | 3 | 0 | 13-Jan-15 A | 23-Mar-15 A | |
| MPP-1022 | (A) Complete Elevation 40 (pool south elevation, L3-L | 5 | 0 | 13-Jan-15 A | 20-Jan-15 A | |
| L05-8226 | Install base at corridors | 1 | 0 | 13-Jan-15 A | 13-Jan-15 A | |
| L16-8138 | Bathrooms - Install toilet accessories | 2 | 0 | 14-Jan-15 A | 15-Jan-15 A | |
| L14-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| CO-7246 | Cx - Heat Pump Start-Up - Levels 9 & 10 | 5 | 0 | 14-Jan-15 A | 16-Jan-15 A | |
| I-5604 | GWB hang, tape & finish FCC ceiling | 5 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| I-5076 | RFI 860.1 - Southeast Elevation Conflict | 1 | 0 | 14-Jan-15 A | 17-Mar-15 A | |
| I-5078 | RFI 884 - Pedestrian Light Pole Base and Drain Conf | 1 | 0 | 14-Jan-15 A | 28-Jan-15 A | |
| L14-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 15-Jan-15 A | 16-Jan-15 A | |
| L16-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 15-Jan-15 A | 21-Jan-15 A | |
| SW-2126 | Zone 1 - Remove temporary transformer | 5 | 0 | 15-Jan-15 A | 28-Jan-15 A | |

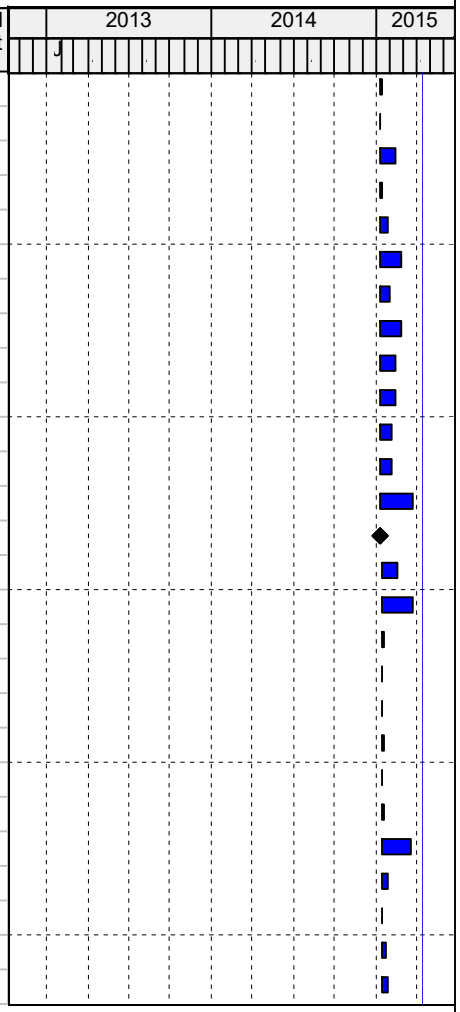


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-5112 | Bar radius ceiling - complete framing | 5 | 0 | 15-Jan-15 A | 20-Jan-15 A | |
| I-5080 | RFI 889 - Site Channelization Plan | 1 | 0 | 15-Jan-15 A | 11-Mar-15 A | |
| L07-8226 | Install base at corridors | 1 | 0 | 16-Jan-15 A | 16-Jan-15 A | |
| I-5060 | RFI 834.1 - NE Retaining Wall Design Clarifications - ( | 1 | 0 | 16-Jan-15 A | 02-Feb-15 A | |
| L16-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| CO-7248 | Cx - Heat Pump Start-Up - Levels 11 & 12 | 5 | 0 | 19-Jan-15 A | 21-Jan-15 A | |
| CO-7254 | Cx - Start-Up - MUA AAON (8) | 5 | 0 | 19-Jan-15 A | 20-Feb-15 A | |
| SW-2020 | Porte Cochere - EIFS at ceiling | 7 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L02-8146 | GWB tape & finish at Locker Rooms | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L1K-8138 | Complete GWB hang & tape | 9 | 0 | 19-Jan-15 A | 06-Feb-15 A | |
| L1L-8252 | Complete electrical/fire alarm rough-in @ ceilings | 3 | 0 | 19-Jan-15 A | 26-Jan-15 A | |
| LL1-8122 | Paint corridors | 6 | 0 | 19-Jan-15 A | 21-Jan-15 A | |
| L1B-6027 | Framing, ceiling at East Ballroom | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L09-8226 | Install base at corridors | 1 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| GB410-102 | Complete painting - Levels 4-10 | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL1-Z2-8110 | Paint, prime & first coat finish at Meeting Rooms | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| I-5122 | Dining feature wall - complete framing | 3 | 0 | 19-Jan-15 A | 21-Jan-15 A | |
| I-5162 | ASI 63 electrical revisions - demo existing | 1 | 0 | 19-Jan-15 A | 19-Jan-15 A | |
| L1B-8170 | Complete cover inspections | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L17-8138 | Bathrooms - Install toilet accessories | 2 | 0 | 20-Jan-15 A | 31-Mar-15 A | |
| MPP-1014 | Caulking - Elevation 1/2/A/B/C/23/24/25 (west elevati | 9 | 0 | 20-Jan-15 A | 30-Jan-15 A | |
| CO-7232 | Cx - TAB - CW Pump Totalization | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| L03-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| LL1-8202 | HVAC trim at ceiling | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| LL1-8206 | Lighting & electrical trim | 4 | 0 | 20-Jan-15 A | 28-Jan-15 A | |
| LL1-8208 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| LL1-Z2-8138 | Paint corridors | 3 | 0 | 20-Jan-15 A | 04-Feb-15 A | |

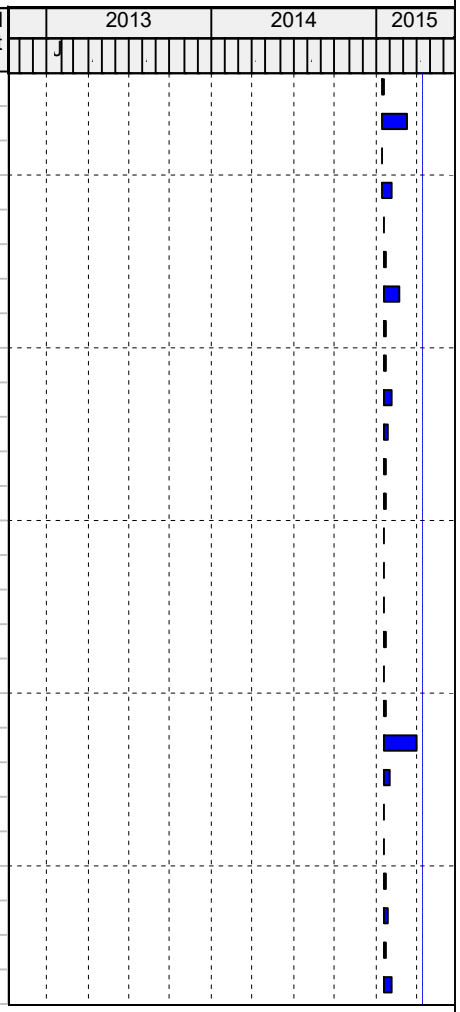



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8226 | Install base at corridors | 1 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| GB410-106 | Complete flooring - Levels 4-10 | 3 | 0 | 20-Jan-15 A | 26-Jan-15 A | |
| L04-8422 | Floor prep | 1 | 0 | 20-Jan-15 A | 02-Feb-15 A | |
| I-5606 | Paint FCC ceiling | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| I-5104 | Bar lighting layout - complete elecrical rough-in | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| I-5164 | ASI 63 electrical revisions - revise electrical | 3 | 0 | 20-Jan-15 A | 02-Feb-15 A | |
| L16-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| CO-7234 | Cx - TAB - CW Water Balancing | 10 | 0 | 21-Jan-15 A | 06-Mar-15 A | |
| L15-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L14-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L12-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L11-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L16-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| CO-7250 | Cx - Heat Pump Start-Up - Levels 14 & 15 | 5 | 0 | 21-Jan-15 A | 23-Jan-15 A | |
| L16-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| I-5304 | Heat Pump Revision - rework GWB | 9 | 0 | 21-Jan-15 A | 30-Jan-15 A | |
| L03-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L04-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L05-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L06-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L07-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L08-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L09-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L11-8226 | Install base at corridors | 1 | 0 | 21-Jan-15 A | 22-Jan-15 A | |
| L05-8422 | Floor prep | 1 | 0 | 21-Jan-15 A | 02-Feb-15 A | |
| ASI65 | ASI No. 65 - Framing Revisions at Foyer 101 | 0 | 0 | 21-Jan-15 A | | |
| L07-7134 | Flooring - VCT | 1 | 0 | 22-Jan-15 A | 22-Jan-15 A | |

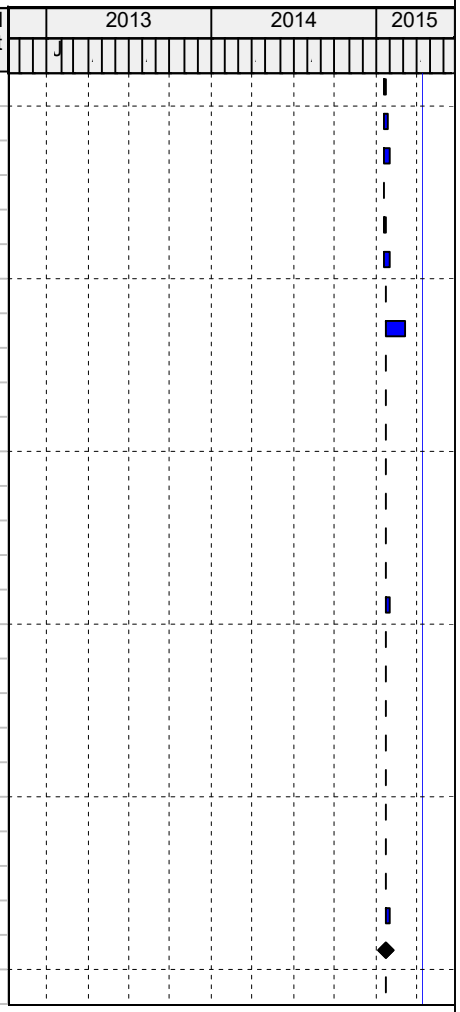



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 22-Jan-15 A | 27-Jan-15 A | |
| LL1-8210 | Fire sprinkler trim | 1 | 0 | 22-Jan-15 A | 22-Jan-15 A | |
| L12-8226 | Install base at corridors | 1 | 0 | 22-Jan-15 A | 23-Jan-15 A | |
| L05-7134 | Flooring - VCT | 1 | 0 | 23-Jan-15 A | 23-Jan-15 A | |
| MPP-1016 | Caulking - Elevation 7/8 (east elevation) | 8 | 0 | 23-Jan-15 A | 24-Feb-15 A | |
| LL1-Z2-8120 | GWB hang, tape & finish ceiling clouds at Jr. Ballroon | 7 | 0 | 23-Jan-15 A | 17-Feb-15 A | |
| LL1-Z3-8148 | Paint Restrooms | 3 | 0 | 23-Jan-15 A | 26-Jan-15 A | |
| MPT-1104 | (B) Install alcoves, east (Elev. 7/8) | 2 | 0 | 23-Jan-15 A | 09-Feb-15 A | |
| L06-8422 | Floor prep | 1 | 0 | 23-Jan-15 A | 23-Jan-15 A | |
| L17-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L06-7134 | Flooring - VCT | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| CO-7216 | Cx - Start-Up Fluid Cooler (power, pre-start & start) | 3 | 0 | 26-Jan-15 A | 28-Jan-15 A | |
| L16-8140 | Install window sills | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| L04-8224 | HVAC grilles & registers at corridors | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| MPT-1058 | Elevation 32 hat channel (south elevation, east of ma | 3 | 0 | 26-Jan-15 A | 17-Feb-15 A | |
| MPT-1090 | Caulking - Elevation 40 (pool south elevation, L3-L17 | 9 | 0 | 26-Jan-15 A | 05-Feb-15 A | |
| LL1-8123 | Floor prep | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| SW-2052 | Zone 4 - Waterproof NW planter walls | 4 | 0 | 26-Jan-15 A | 29-Jan-15 A | |
| L1L-8290 | GWB, top rock | 3 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L10-8131 | Bathrooms - Install access panels | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| L14-8226 | Install base at corridors | 1 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| I-5372 | (S) Elevation 32, complete insulation | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| GB1117-100 | Complete GWB - Levels 3, 11-16 | 7 | 0 | 26-Jan-15 A | 30-Jan-15 A | |
| SW-2322 | Zone 3 - FRP landscape curb at exit door | 5 | 0 | 26-Jan-15 A | 30-Jan-15 A | |
| I-6010 | RFI 901 - Pool topping slab issue (Owner procure floc | 10 | 0 | 26-Jan-15 A | 03-Apr-15 A | |
| L03-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L16-7034 | Install doors & hardware (x42) | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |

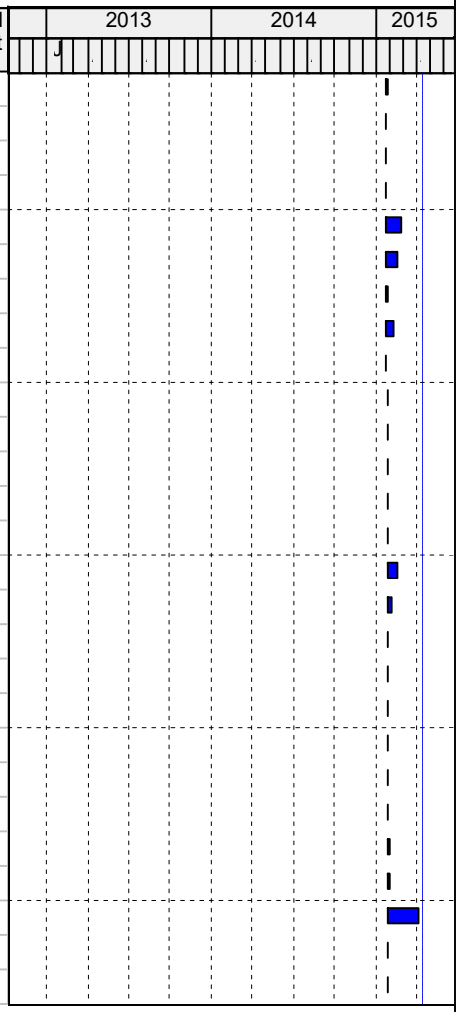



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7034 | Install doors & hardware (x42) | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L08-7134 | Flooring - VCT | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L16-7138 | Electrical trim & finish | 1 | 0 | 27-Jan-15 A | 18-Feb-15 A | |
| L17-7136 | Install doors & hardware | 1 | 0 | 27-Jan-15 A | 17-Feb-15 A | |
| I-1640 | Manlift finishes - Install window sills | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L03-8668 | Remove scaffolding at pool pit | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L17-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L11-8131 | Bathrooms - Install access panels | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L15-8226 | Install base at corridors | 1 | 0 | 27-Jan-15 A | 28-Jan-15 A | |
| MPP-1052 | (B) Elevation 3 (south elevation, west of manlift, L1-L: | 5 | 0 | 27-Jan-15 A | 30-Jan-15 A | |
| GB410-108 | Complete base - Levels 4-10 | 4 | 0 | 27-Jan-15 A | 30-Jan-15 A | |
| L08-8422 | Floor prep | 1 | 0 | 27-Jan-15 A | 28-Jan-15 A | |
| I-5132 | Bar plumbing relocation - relocate waste line | 3 | 0 | 27-Jan-15 A | 29-Jan-15 A | |
| I-5152 | Sprinkler pipe furring - install framing around pipe | 2 | 0 | 27-Jan-15 A | 28-Jan-15 A | |
| L09-7134 | Flooring - VCT | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L17-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L17-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| EL-6042 | Elev 6 - Install EMR heat pump | 6 | 0 | 28-Jan-15 A | 25-Feb-15 A | |
| MPT-1056 | Complete Elevation 31 (above L12 terrace, west elev | 3 | 0 | 28-Jan-15 A | 13-Feb-15 A | |
| L1L-8256 | GWB hang walls | 3 | 0 | 28-Jan-15 A | 05-Feb-15 A | |
| SW-2230 | Zone 2 - Repair sidewalk north of 3rd Ave | 5 | 0 | 28-Jan-15 A | 30-Jan-15 A | |
| L12-8131 | Bathrooms - Install access panels | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L08-8226 | Install base at corridors | 1 | 0 | 28-Jan-15 A | 30-Jan-15 A | |
| L16-8226 | Install base at corridors | 1 | 0 | 28-Jan-15 A | 29-Jan-15 A | |
| I-5373 | (S) Elevation 32, install sign backing | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L07-8422 | Floor prep | 1 | 0 | 28-Jan-15 A | 03-Feb-15 A | |
| I-6000 | Resolve cloud framing engineering issue | 5 | 0 | 28-Jan-15 A | 03-Feb-15 A | |

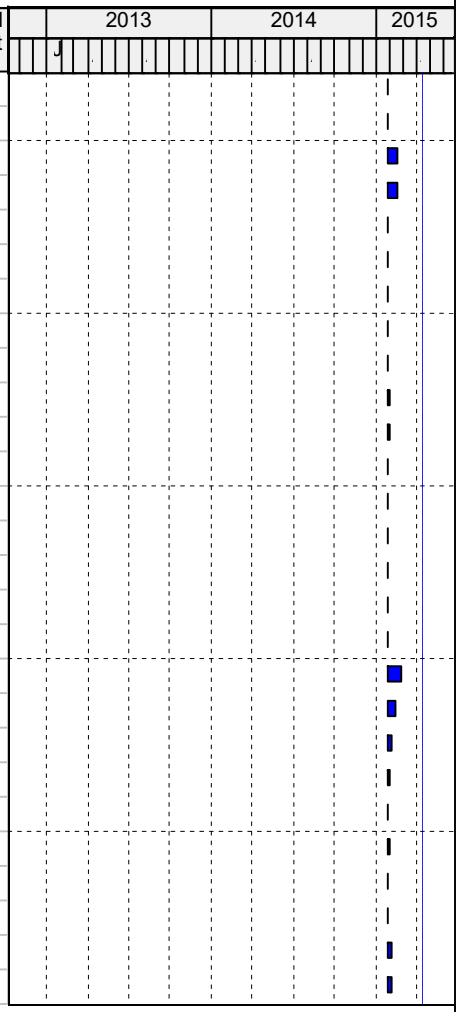



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7134 | Flooring - VCT | 1 | 0 | 29-Jan-15 A | 29-Jan-15 A | |
| L1L-8226 | GWB hang ceilings & complete walls | 3 | 0 | 29-Jan-15 A | 23-Feb-15 A | |
| L1L-8248 | Complete electrical/fire alarm rough-in @ ceilings | 3 | 0 | 29-Jan-15 A | 02-Feb-15 A | |
| L1L-8250 | Complete HVAC RI @ ceilings | 5 | 0 | 29-Jan-15 A | 04-Feb-15 A | |
| L03-8218 | Install base at corridors | 1 | 0 | 29-Jan-15 A | 30-Jan-15 A | |
| MPP-1062 | (C) Install level 3 cornice metal (Porte Cochere) | 2 | 0 | 29-Jan-15 A | 04-Feb-15 A | |
| EL-6040 | Elev 6 - Install machine room controller equipment/hy | 3 | 0 | 30-Jan-15 A | 24-Feb-15 A | |
| EL-6054 | Elev 6 - Install EMR doors, hardware & labeling | 2 | 0 | 30-Jan-15 A | 23-Feb-15 A | |
| LL1-8160 | Flooring - carpet | 10 | 0 | 30-Jan-15 A | 18-Feb-15 A | |
| I-5472 | Reframe Laundry Room ceiling (per ceiling height RF | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5474 | Restore Laundry Room GWB (hang & tape) (per ceili | 5 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5476 | Repaint Laundry Room ceiling | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5478 | Demo existing Laundry Room ceiling | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5480 | Revise MEP above Laundry Room ceiling | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5134 | Bar plumbing relocation - adust framing | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5136 | Bar plumbing relocation - GWB hang, tape & finish [D | 7 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5138 | Bar plumbing relocation - paint [DELETED] | 2 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5142 | Damper at BPF #8 - mechanical revisions | 2 | 0 | 30-Jan-15 A | 02-Feb-15 A | |
| L04-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 02-Feb-15 A | 02-Feb-15 A | |
| L04-7134 | Flooring - VCT | 1 | 0 | 02-Feb-15 A | 02-Feb-15 A | |
| LL1-8124a | Install base | 10 | 0 | 02-Feb-15 A | 23-Feb-15 A | |
| CO-7218 | Cx - Heat Pump Start-Up - Levels 16 & 17 | 5 | 0 | 02-Feb-15 A | 04-Feb-15 A | |
| LL1-6014Id | L1 bar redesign - paint ceilings at Excercise & MR9 | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| EL-1236 | Elev 1&2 - Walsh/TKE pre-inspection | 6 | 0 | 02-Feb-15 A | 27-Feb-15 A | |
| MPT-1050 | (B) Install louvers, east | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| MPT-1070 | Tower Sign, East (El. 44) | 5 | 0 | 02-Feb-15 A | 10-Feb-15 A | |
| L1L-8272 | GWB hang ceilings | 3 | 0 | 02-Feb-15 A | 04-Feb-15 A | |

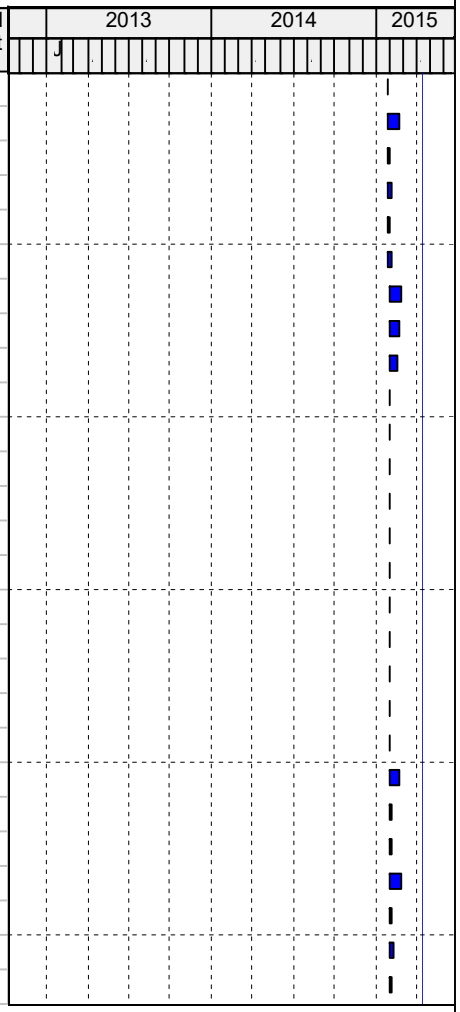



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2320 | Zone 3 - Pour ped pole base | 3 | 0 | 02-Feb-15 A | 05-Feb-15 A | |
| LL1-8156 | Install doors & hardware at corridors | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| L1B-6015 | HVAC drops at West Ballrooms | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L1B-6021 | Electrical drops at West Ballrooms | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L1B-6029 | HVAC drops at East Ballroom | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L1B-6031 | Electrical drops at East Ballroom | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L06-8226 | Install base at corridors | 1 | 0 | 02-Feb-15 A | 02-Feb-15 A | |
| GB410-104 | Complete vinyl wallcoverings - Levels 4-10 | 4 | 0 | 02-Feb-15 A | 17-Feb-15 A | |
| GB1117-102 | Complete painting - Levels 3, 11-16 | 3 | 0 | 02-Feb-15 A | 04-Feb-15 A | |
| SW-2234 | Zone 2 - FRP door curbs | 4 | 0 | 02-Feb-15 A | 05-Feb-15 A | |
| I-6950 | Resolve MEP/ceiling height conflicts | 1 | 0 | 02-Feb-15 A | 13-Mar-15 A | |
| L05-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L04-7138 | Electrical trim & finish | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L05-7138 | Electrical trim & finish | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L11-7134 | Flooring - VCT | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| SW-2022 | Zone 4 - Remove pedestrian protection on 110th Ave | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L1L-8246 | Complete fire sprinkler RI @ ceilings | 2 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| LL1-8184 | Install storefront at Exercise Room | 1 | 0 | 03-Feb-15 A | 02-Mar-15 A | |
| L12-8422 | Floor prep | 1 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| L14-8422 | Floor prep | 1 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| L15-8422 | Floor prep | 1 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| I-5144 | Damper at BPF #8 - framing revisions | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| I-5154 | Sprinkler pipe furring - GWB hang | 7 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| I-5166 | ASI 63 electrical revisions - insulation | 2 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| ASI62r1 | ASI No. 62 (Revised) - Civil Site Grading Revisions an | 0 | 0 | 03-Feb-15 A | | |
| L06-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 04-Feb-15 A | 04-Feb-15 A | |
| L12-7134 | Flooring - VCT | 1 | 0 | 04-Feb-15 A | 04-Feb-15 A | |

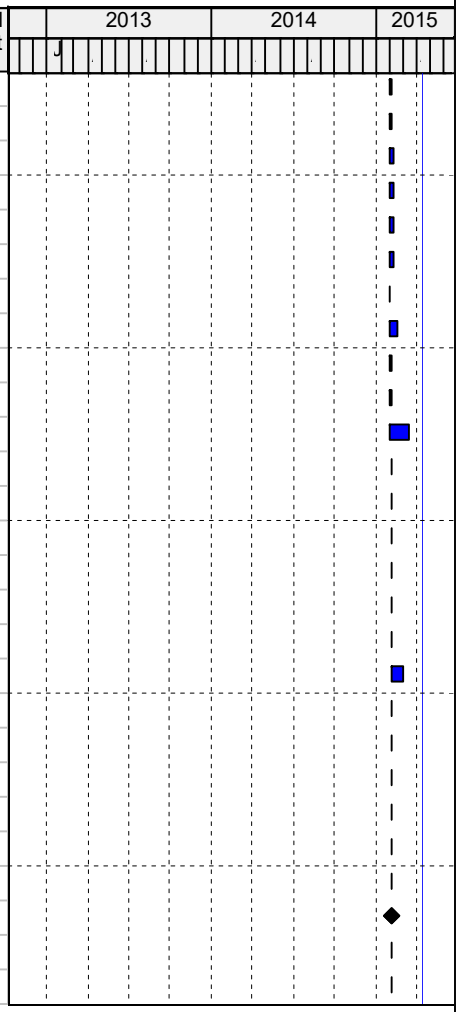



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8142 | Ceramic tile in restrooms | 7 | 0 | 04-Feb-15 A | 20-Feb-15 A | |
| L1K-8144 | Paint, prime & first coat finish | 3 | 0 | 04-Feb-15 A | 09-Mar-15 A | |
| LL1-Z2-8158 | Wall coverings - vinyl at Meeting Rooms | 2 | 0 | 04-Feb-15 A | 05-Feb-15 A | |
| L09-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 06-Feb-15 A | |
| L10-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 09-Feb-15 A | |
| L11-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 09-Feb-15 A | |
| L16-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 10-Feb-15 A | |
| I-5146 | Damper at BPF #8 - complete GWB hang | 1 | 0 | 04-Feb-15 A | 04-Feb-15 A | |
| I-5168 | ASI 63 electrical revisions - vapor barrier | 2 | 0 | 04-Feb-15 A | 05-Feb-15 A | |
| L07-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 05-Feb-15 A | 05-Feb-15 A | |
| L14-7134 | Flooring - VCT | 1 | 0 | 05-Feb-15 A | 05-Feb-15 A | |
| L1L-8102a | GWB tape & finish walls & ceilings (Dining & Lounge) | 7 | 0 | 05-Feb-15 A | 12-Feb-15 A | |
| LL1-8170 | Flooring - tile at elevator lobby | 3 | 0 | 05-Feb-15 A | 09-Feb-15 A | |
| LL1-8186 | Wall coverings - vinyl at corridors | 5 | 0 | 05-Feb-15 A | 19-Feb-15 A | |
| L1B-6023 | Fire sprinkler drops at West Ballrooms | 5 | 0 | 05-Feb-15 A | 09-Feb-15 A | |
| L1B-6033 | Fire sprinkler drops at East Ballroom | 5 | 0 | 05-Feb-15 A | 09-Feb-15 A | |
| GB1117-106 | Complete flooring - Levels 3, 11-16 | 4 | 0 | 05-Feb-15 A | 10-Feb-15 A | |
| I-6100 | Resolve lighting/access panel conflict | 5 | 0 | 05-Feb-15 A | 13-Feb-15 A | |
| GB1117-104 | Complete vinyl wallcoverings - Levels 3, 11-16 | 5 | 0 | 05-Feb-15 A | 11-Feb-15 A | |
| L08-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 06-Feb-15 A | 06-Feb-15 A | |
| L15-7134 | Flooring - VCT | 1 | 0 | 06-Feb-15 A | 06-Feb-15 A | |
| MPP-1054 | Caulking - Elevation 3 (south elevation, west of manli | 3 | 0 | 06-Feb-15 A | 10-Feb-15 A | |
| ASI66 | ASI No. 66 - MDP Electrical Drawings Revision 23A | 0 | 0 | 06-Feb-15 A | | |
| L03-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L04-8408 | Install base at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L05-8408 | Install base at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L06-8408 | Install base at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |

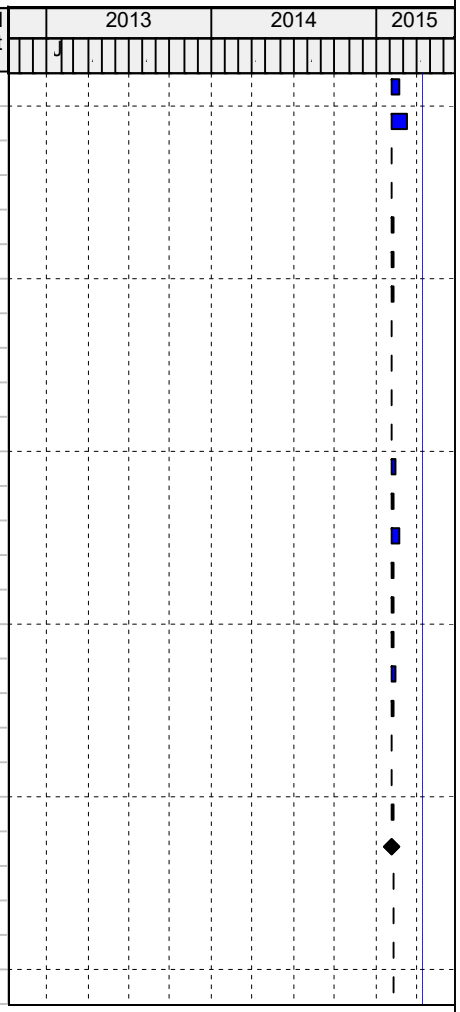



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L16-7134 | Flooring - VCT | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L1K-8102a | GWB hang ceilings at Public Restroom | 2 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| LL2-2094 | Install doors & hardware at Laundry | 2 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| SW-2032 | Zone 4 - Demo existing trees & hardscapes | 3 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| CO-7139 | Install remaining devices & prep devices for testing - | 7 | 0 | 09-Feb-15 A | 03-Mar-15 A | |
| MPP-1024 | (B) Complete Elevation 4 (south elevation, east of tov | 2 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| L1L-8218 | Frame ceilings & inspection | 5 | 0 | 09-Feb-15 A | 12-Feb-15 A | |
| L1K-8136 | Ceiling grid & inspection | 4 | 0 | 09-Feb-15 A | 11-Feb-15 A | |
| L1L-8274 | GWB tape & finish walls & ceilings | 7 | 0 | 09-Feb-15 A | 24-Feb-15 A | |
| L15-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L16-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L17-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L14-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| I-5170 | ASI 63 electrical revisions - GWB hang, tape & finish | 7 | 0 | 09-Feb-15 A | 17-Feb-15 A | |
| SW-2058 | Zone 4 - Demo existing curb at 110th | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| MPT-1114 | Cap metal - Porte Cochere | 3 | 0 | 09-Feb-15 A | 12-Feb-15 A | |
| I-5172 | Resolve Bar Area RFIs & complete revised work | 10 | 0 | 09-Feb-15 A | 04-Mar-15 A | |
| I-2960 | Lack of Stainless Steel Ceiling Closure Pieces (Shrou | 5 | 0 | 09-Feb-15 A | 13-Mar-15 A | |
| L07-8408 | Install base at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L08-8408 | Install base at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L09-8408 | Install base at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L10-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L11-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L17-7134 | Flooring - VCT | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L09-8224 | HVAC grilles & registers at corridors | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L08-8224 | HVAC grilles & registers at corridors | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |

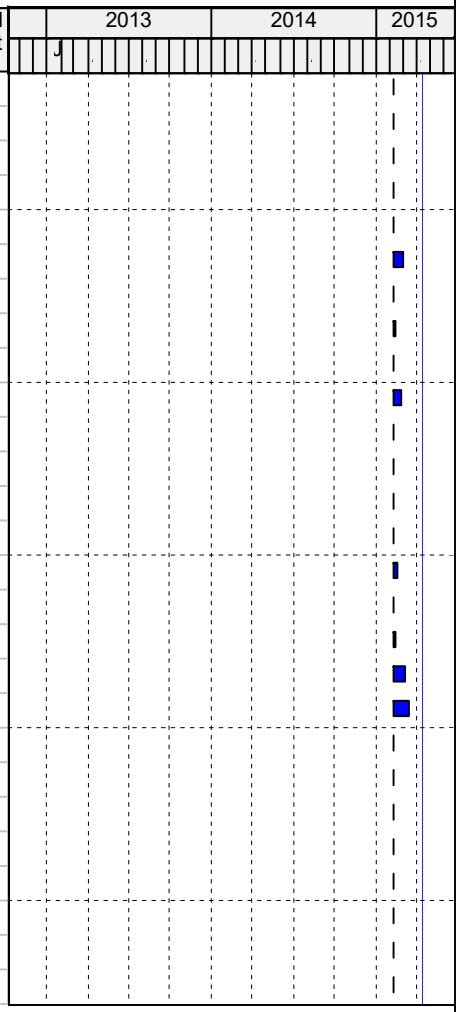



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8224 | HVAC grilles & registers at corridors | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| SW-2036 | Zone 4 - Grade for curb and gutter | 2 | 0 | 10-Feb-15 A | 11-Feb-15 A | |
| CO-7140 | Fire Alarm System Device Testing - Tower Levels 4 thı | 7 | 0 | 10-Feb-15 A | 05-Mar-15 A | |
| L17-8422 | Floor prep | 1 | 0 | 10-Feb-15 A | 11-Feb-15 A | |
| MPT-1116 | Cap metal - Pool high roof | 3 | 0 | 10-Feb-15 A | 12-Feb-15 A | |
| ASI67 | ASI No. 67 - Meeting Room Door Hardware Revisions | 0 | 0 | 10-Feb-15 A | | |
| L10-8408 | Install base at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L11-8408 | Install base at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L12-8408 | Install base at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L12-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L14-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L03-7134 | Flooring - VCT | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| MPT-1018a | Install hi-roof cornice metal | 8 | 0 | 11-Feb-15 A | 08-Apr-15 A | |
| SW-2038 | Zone 4 - FRP curb & gutter | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| SW-2046 | Zone 4 - Install conduit | 2 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L1K-8152 | Install doors & hardware | 3 | 0 | 11-Feb-15 A | 17-Feb-15 A | |
| L1L-8228 | GWB tape & finish | 7 | 0 | 11-Feb-15 A | 03-Mar-15 A | |
| SW-2054 | Zone 4 - Install flag pole bases | 3 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| L17-8226 | Install base at corridors | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| MPP-1058 | (B) Install podium cornice, south/east | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| L03-8422 | Floor prep | 1 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| MPT-1108 | Cap metal - complete at tower | 5 | 0 | 11-Feb-15 A | 13-Feb-15 A | |
| MPT-1112 | Cap metal - complete at Ballroom roof | 3 | 0 | 11-Feb-15 A | 13-Feb-15 A | |
| CO-7404 | Cx - FPT - Heat Pumps | 3 | 0 | 11-Feb-15 A | 13-Feb-15 A | |
| L14-8408 | Install base at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L15-8408 | Install base at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L15-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |

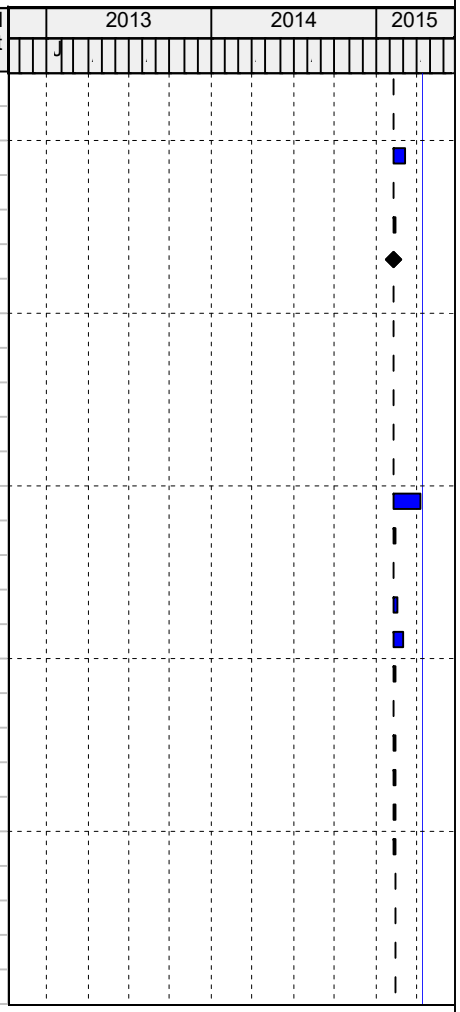



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8408 | Install base at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L16-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L06-7138 | Electrical trim & finish | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L1K-8102b | GWB tape & finish at Restrooms | 7 | 0 | 12-Feb-15 A | 25-Feb-15 A | |
| LL1-8154 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 12-Feb-15 A | 20-Feb-15 A | |
| ASI68 | ASI No. 68 - MDP Mechanical Drawings Revision 21 | 0 | 0 | 12-Feb-15 A | | |
| LL1-Z3-FCC28 | Electrical trim & finish at FCC | 4 | 0 | 12-Feb-15 A | 16-Feb-15 A | |
| LL1-8182 | Install doors & hardware at Exercise Room | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| GB1117-108 | Complete base - Levels 3, 11-16 | 5 | 0 | 12-Feb-15 A | 18-Feb-15 A | |
| GB1117-110 | Complete countertops - Levels 3, 11-16 | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| GB1117-112 | Complete shower/tub surrounds - Levels 3, 11-16 | 3 | 0 | 12-Feb-15 A | 16-Feb-15 A | |
| L17-8408 | Install base at Elevator Lobby | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| L17-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| SW-2118 | Zone 1 - FRP sidewalk (NE corner) | 2 | 0 | 13-Feb-15 A | 13-Mar-15 A | |
| SW-2034 | Zone 4 - Install irrigation sleeves | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| SW-2060 | Zone 4 - Sawcut curb & gutter | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| ASI69 | ASI No. 69 - Architectural Level 1 Revised Ceiling Plai | 0 | 0 | 13-Feb-15 A | | |
| LL1-Z2-8142 | Wall coverings - vinyl at corridors | 3 | 0 | 16-Feb-15 A | 19-Feb-15 A | |
| I-6900 | Resolve Garage EF motor/VFD issue (including corre | 20 | 0 | 16-Feb-15 A | 25-Mar-15 A | |
| I-5066 | RFI 848.1 -Flagpole Lighting - South Light/Flagpole E | 1 | 0 | 16-Feb-15 A | 16-Mar-15 A | |
| L03-7136 | Install doors & hardware | 2 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| MPP-1012 | Caulking - Elevation 4 (south elevation, east of tower) | 6 | 0 | 16-Feb-15 A | 23-Feb-15 A | |
| L10-8224 | HVAC grilles & registers at corridors | 1 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| L06-8224 | HVAC grilles & registers at corridors | 1 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| L05-8224 | HVAC grilles & registers at corridors | 1 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| SW-2040 | Zone 4 - Fine grade for sidewalk and planter curb | 3 | 0 | 16-Feb-15 A | 17-Feb-15 A | |
| MPP-1036 | Podium Signs, East | 5 | 0 | 16-Feb-15 A | 18-Feb-15 A | |

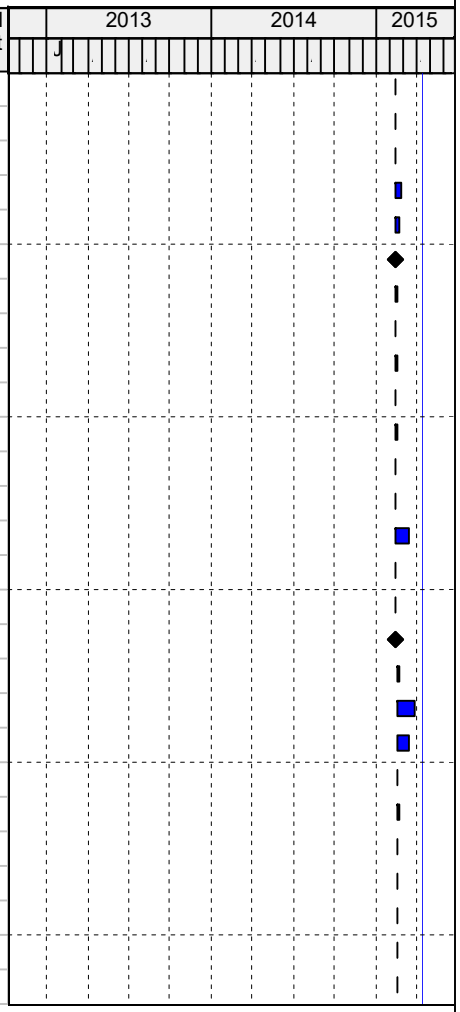



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8150 | HVAC drops/trim at ceiling | 2 | 0 | 16-Feb-15 A | 17-Feb-15 A | |
| LL2-8146 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 16-Feb-15 A | 23-Feb-15 A | |
| LL1-8172 | Ceiling grid & inspection at Exercise Room (additional | 6 | 0 | 16-Feb-15 A | 23-Feb-15 A | |
| L1K-8162 | Complete wallcoverings (FRP) | 2 | 0 | 16-Feb-15 A | 17-Feb-15 A | |
| L1B-6011 | GWB, hang ceiling at West Ballrooms | 4 | 0 | 16-Feb-15 A | 18-Feb-15 A | |
| L1B-8138 | GWB hang, tape & finish ceilings at corridors (comple | 11 | 8 | 16-Feb-15 A | 29-Apr-15 | 0 |
| LL1-8176 | HVAC drops/trim to grid | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L03-8408 | Install base at Elevator Lobby | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L03-7034 | Install doors & hardware (x42) | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L03-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L07-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L08-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L09-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L10-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L11-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L12-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L16-7136 | Install doors & hardware | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| LL2-2062 | Ceiling grid at Laundry | 4 | 0 | 17-Feb-15 A | 30-Mar-15 A | |
| L15-8224 | HVAC grilles & registers at corridors | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L14-8224 | HVAC grilles & registers at corridors | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| CO-7258 | Cx - Start-Up - KMUA Trane (2) | 2 | 0 | 17-Feb-15 A | 20-Feb-15 A | |
| SW-2044 | Zone 4 - FRP sidewalk (SW corner remaining) | 3 | 0 | 17-Feb-15 A | 02-Apr-15 A | |
| LL1-Z3-FCC30 | Data/phone trim/finish at FCC | 4 | 0 | 17-Feb-15 A | 19-Feb-15 A | |
| LL1-Z3-6036 | GWB hang, tape & finish ceiling at Food Prep (Dry St | 5 | 0 | 17-Feb-15 A | 02-Mar-15 A | |
| MPT-1092 | Caulking - Elevation 31 (above L12 terrace, west elev | 4 | 0 | 17-Feb-15 A | 20-Feb-15 A | |
| MPT-1098 | Caulking - Elevation 30 (south elevation, west of man | 6 | 0 | 17-Feb-15 A | 23-Mar-15 A | |
| LL1-6014Id2 | L1 bar redesign - install wall coverings at MR9 | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |

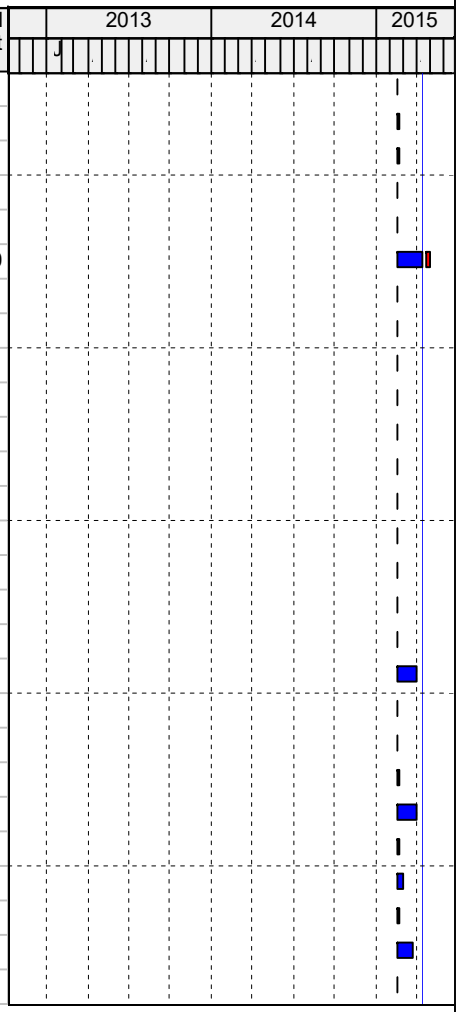



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8146 | Fire sprinkler drops/trim at ceiling | 1 | 0 | 17-Feb-15 A | 10-Mar-15 A | |
| L1K-8148 | Lighting & electrical trim at ceiling | 2 | 0 | 17-Feb-15 A | 10-Mar-15 A | |
| GB1117-114 | Complete plumbing fixture installation - Levels 3, 11-1 | 4 | 0 | 17-Feb-15 A | 20-Feb-15 A | |
| L1K-8164 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 17-Feb-15 A | 10-Mar-15 A | |
| MPT-1062 | Elevation 32 metal panels (south elevation, east of m | 8 | 0 | 18-Feb-15 A | 26-Mar-15 A | |
| L14-7138 | Electrical trim & finish | 1 | 0 | 18-Feb-15 A | 18-Feb-15 A | |
| L15-7138 | Electrical trim & finish | 1 | 0 | 18-Feb-15 A | 18-Feb-15 A | |
| L17-7138 | Electrical trim & finish | 1 | 0 | 18-Feb-15 A | 18-Feb-15 A | |
| CO-7262 | Cx - Start-Up - Electric Unit Heaters | 3 | 0 | 18-Feb-15 A | 30-Mar-15 A | |
| LL1-8174 | Wall coverings - vinyl at Exercise Room | 2 | 0 | 18-Feb-15 A | 19-Feb-15 A | |
| L1B-6017 | GWB, hang ceiling at East Ballrooms | 4 | 0 | 18-Feb-15 A | 20-Feb-15 A | |
| SW-2062 | Zone 4 - Patch curb & gutter | 2 | 0 | 18-Feb-15 A | 19-Feb-15 A | |
| CO-7256 | Cx - Start-Up - Elevator Machine Room Ductless Split | 1 | 0 | 19-Feb-15 A | 19-Feb-15 A | |
| LL1-8178 | Lighting & electrical drops to grid | 2 | 0 | 19-Feb-15 A | 20-Feb-15 A | |
| LL1-8180 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 19-Feb-15 A | 20-Feb-15 A | |
| GB410-110 | Complete countertops - Levels 4-10 | 1 | 0 | 19-Feb-15 A | 19-Feb-15 A | |
| GB410-112 | Complete shower/tub surrounds - Levels 4-10 | 1 | 0 | 19-Feb-15 A | 19-Feb-15 A | |
| GB410-118 | Complete barn doors - Levels 4-10 | 1 | 0 | 19-Feb-15 A | 19-Feb-15 A | |
| GB1117-118 | Complete barn doors - Levels 3, 11-16 | 2 | 0 | 19-Feb-15 A | 20-Feb-15 A | |
| LL1-Z2-8160a | Flooring - carpet at Meeting Rooms | 2 | 0 | 19-Feb-15 A | 23-Feb-15 A | |
| LL2-2098 | HVAC drops to grid at Laundry | 2 | 0 | 20-Feb-15 A | 04-Mar-15 A | |
| LL2-2088 | Lighting & electrical drops to grid at Laundry | 2 | 0 | 20-Feb-15 A | 09-Mar-15 A | |
| L1K-8123 | Floor prep | 2 | 0 | 20-Feb-15 A | 23-Feb-15 A | |
| LL1-8158 | Floor prep at corridors | 2 | 0 | 20-Feb-15 A | 23-Feb-15 A | |
| L1B-8102a | GWB, tape & finish ceiling at West Ballroom | 7 | 0 | 20-Feb-15 A | 02-Mar-15 A | |
| GB410-114 | Complete plumbing fixture installation - Levels 4-10 | 3 | 0 | 20-Feb-15 A | 24-Feb-15 A | |
| LL2-2106 | Floor prep | 1 | 0 | 20-Feb-15 A | 20-Feb-15 A | |

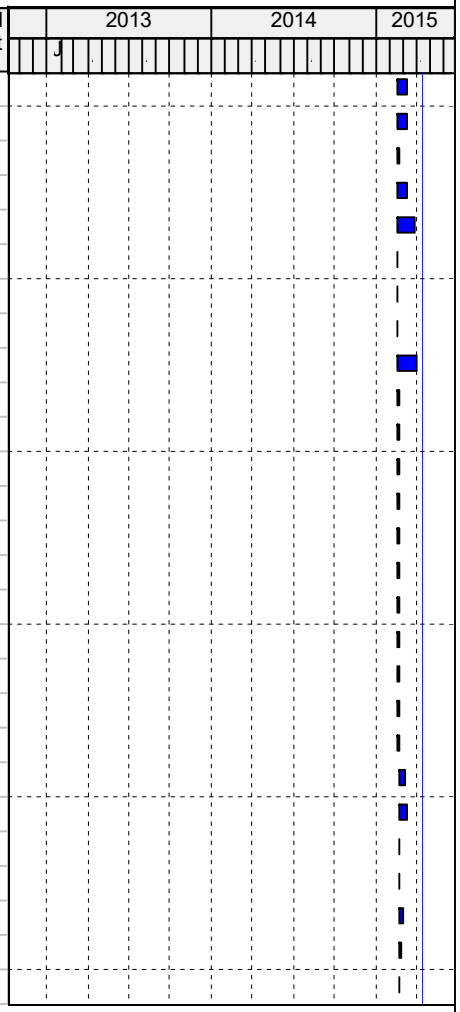



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2086 | Flooring - epoxy remainder of floor (including prep) | 6 | 0 | 21-Feb-15 A | 26-Feb-15 A | |
| MPT-1102 | Elevation 32 spandrel panels (south elevation, east o | 2 | 0 | 21-Feb-15 A | 16-Mar-15 A | |
| LL2-2104 | Flooring - epoxy at equipment alcoves | 5 | 0 | 21-Feb-15 A | 26-Feb-15 A | |
| LL1-Z3-8164 | Field measure & fabricate countertops | 15 | 5 | 21-Feb-15 A | 17-Apr-15 | 7 |
| LL1-8116f | Fabricate & deliver countertops | 10 | 5 | 21-Feb-15 A | 17-Apr-15 | 12 |
| LL1-Z2-8118a | Install decorative light fixtures | 3 | 0 | 23-Feb-15 A | 03-Mar-15 A | |
| LL1-Z2-8124a | Install base | 10 | 0 | 23-Feb-15 A | 27-Feb-15 A | |
| CO-7400 | Cx - 3rd Party Cx of Mechanical, Plumbing, Electrical | 40 | 15 | 23-Feb-15 A | 01-May-15 | 5 |
| LL1-Z3-8144 | Install toilets at Restrooms | 4 | 0 | 23-Feb-15 A | 27-Feb-15 A | |
| LL1-8166 | Install base at corridors | 5 | 0 | 23-Feb-15 A | 27-Feb-15 A | |
| LL1-Z2-8122 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 23-Feb-15 A | 09-Mar-15 A | |
| GB1117-116 | Complete shower doors - Levels 3, 11-16 | 2 | 0 | 23-Feb-15 A | 24-Feb-15 A | |
| L17-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| L16-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| L12-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| L11-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| L03-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| MPT-1100 | Install spandrel, east (Elevation 44) | 2 | 0 | 24-Feb-15 A | 26-Feb-15 A | |
| SW-2064 | Porte Cochere - Fill and grade Porte Cochere drive | 3 | 0 | 24-Feb-15 A | 06-Mar-15 A | |
| L1BOH2-8104 | Paint, prime | 2 | 1 | 24-Feb-15 A | 13-Apr-15 | 5 |
| L1K-8124a | Flooring - epoxy - east end | 5 | 0 | 24-Feb-15 A | 26-Feb-15 A | |
| LL2-8148 | Fire sprinkler drops to grid | 1 | 0 | 24-Feb-15 A | 09-Mar-15 A | |
| LL1-8162 | Flooring - carpet at corridors | 5 | 0 | 24-Feb-15 A | 02-Mar-15 A | |
| LL1-Z2-8128 | HVAC trim at ceiling | 1 | 0 | 24-Feb-15 A | 03-Mar-15 A | |
| LL1-Z2-8130 | Fire sprinkler trim | 1 | 0 | 24-Feb-15 A | 04-Mar-15 A | |
| MPT-1052 | Elevation 48/49 (north elevation, east of 51, L3-L17) | 3 | 0 | 25-Feb-15 A | 11-Mar-15 A | |
| CO-7100T | Cx - Start-Up - Life Safety Exhaust Fans and VFD's | 13 | 0 | 25-Feb-15 A | 03-Apr-15 A | |

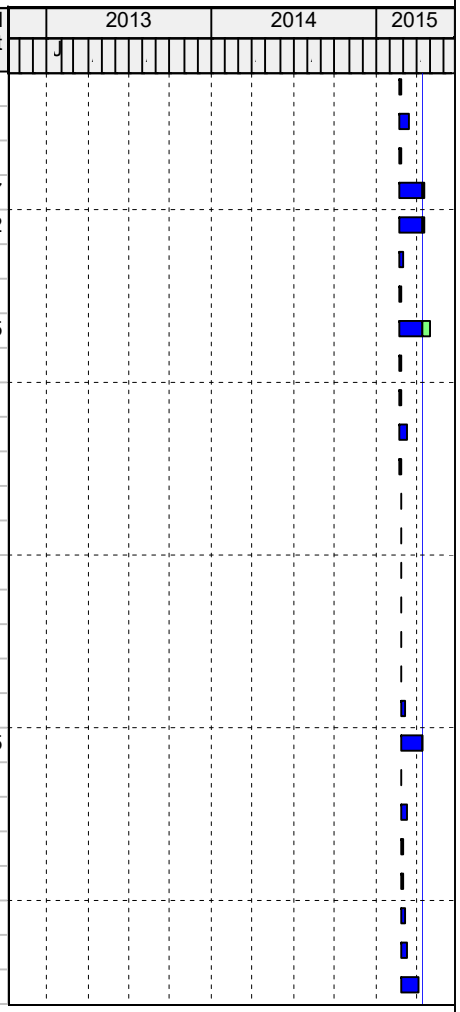



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6044 | Elev 6 - Electrical trim & finish | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| EL-6046 | Elev 6 - Fire alarm trim | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| EL-6048 | Elev 6 - Fire sprinkler trim | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| EL-6050 | Elev 6 - Install pit grates | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| L1L-8276 | Paint, prime & first coat finish | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| GB410-116 | Complete shower doors - Levels 4-10 | 2 | 0 | 25-Feb-15 A | 26-Feb-15 A | |
| L1BOH2-8114 | Ceiling grid & inspection | 4 | 0 | 26-Feb-15 A | 18-Mar-15 A | |
| SW-2066 | Porte Cochere - FRP planter curb | 2 | 0 | 26-Feb-15 A | 27-Feb-15 A | |
| L03-8684 | Pourback piping trench | 1 | 0 | 26-Feb-15 A | 26-Feb-15 A | |
| AS70 | ASI No. 70 - Site Illumination Plan | 0 | 0 | 26-Feb-15 A | | |
| I-5082 | ASI 70 - Site Illumination Plan | 0 | 0 | 26-Feb-15 A | | |
| L1BOH2-8200 | Paint, first coat finish | 1 | 1 | 26-Feb-15 A | 14-Apr-15 | 5 |
| CO-7220 | Cx - Start-Up - Common Space Heat Pump | 4 | 2 | 26-Feb-15 A | 14-Apr-15 | 26 |
| I-3102 | GWB, tape & finish ceiling at East Ballroom | 7 | 0 | 26-Feb-15 A | 06-Mar-15 A | |
| I-5124 | Dining feature wall - install plywood backing | 1 | 0 | 26-Feb-15 A | 26-Feb-15 A | |
| L03-8686 | Cure piping trench | 14 | 0 | 27-Feb-15 A | 12-Mar-15 A | |
| L1L-8114a | Install 9-wood celing supports - south of Grid K | 3 | 0 | 27-Feb-15 A | 04-Mar-15 A | |
| L1K-8124b | Flooring - epoxy - west end (including prep) | 7 | 0 | 27-Feb-15 A | 06-Mar-15 A | |
| CO-7104T | Fire Alarm & Smoke Control Pre-Testing (Tower) - Tow | 3 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7112T | City of Bellevue/3rd Party Fire Sprinkler Inspection / A | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7118T | City of Bellevue/3rd Party Fire Alarm Inspection / Appl | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7106T | City of Bellevue/3rd Party Smoke Control Testing (Tow | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7412 | Cx - Pressure Testing - GC Indicates Podium Complet | 0 | 0 | | 01-Mar-15 A | |
| CO-7416 | Cx - Pressure Testing - Pre-Walk with GC (Podium) [Dl | 1 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7418 | Cx - Pressure Testing - GC Makes Corrections (Podiu | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7420 | Cx - Pressure Testing - Pressure Pre-Test (Podium) [D | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7422 | Cx - Pressure Testing -Corrections (Podium) [DELETE | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |

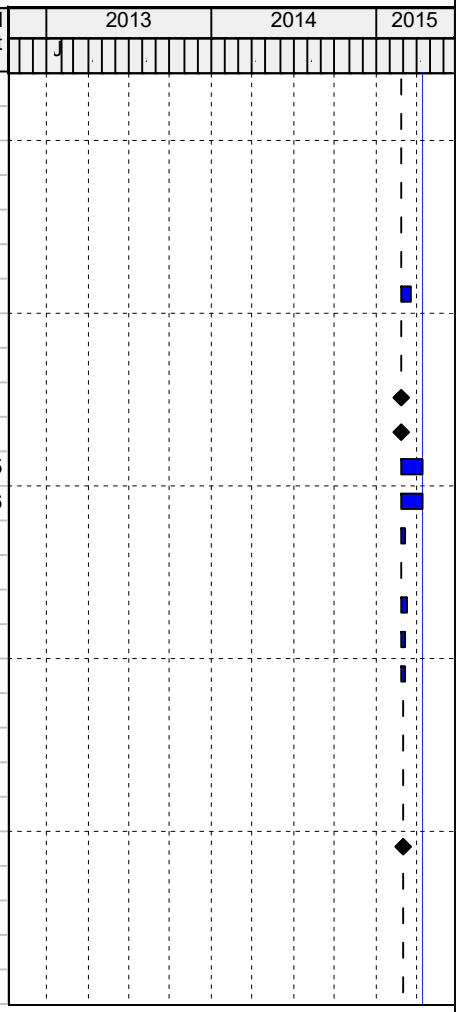


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7424 | Cx - Pressure Testing - Pressure Final Test [DELETED | 1 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7426 | Cx - Pressure Testing - Building Final Corrections [DEI | 1 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7142 | Fire Alarm System Device Testing - Podium [DELETEI | 7 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7428 | Cx - Pressure Testing - GC Indicates Tower Complete | 0 | 0 | | 01-Mar-15 A | |
| CO-7430 | Cx - Pressure Testing - Pre-Walk with GC (Tower) [DEI | 1 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7432 | Cx - Pressure Testing - GC Makes Corrections (Tower) | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7434 | Cx - Pressure Testing - Pressure Pre-Test (Tower) [DEI | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7436 | Cx - Pressure Testing -Corrections (Tower) [DELETED, | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| SW-2042 | Porte Cochere - Install trench drain | 3 | 0 | 02-Mar-15 A | 04-Mar-15 A | |
| SW-2128 | Zone 1 - FRP planter wall at NE corner | 8 | 0 | 02-Mar-15 A | 04-Mar-15 A | |
| SW-2130 | Zone 1 - Waterproof wall | 2 | 0 | 02-Mar-15 A | 02-Mar-15 A | |
| LL1-Z3-FCC36 | Install doors & hardware at FCC | 2 | 0 | 02-Mar-15 A | 02-Mar-15 A | |
| LL1-8136 | Ceramic tile in restrooms | 3 | 0 | 02-Mar-15 A | 04-Mar-15 A | |
| L1K-8218 | Floor prep | 2 | 0 | 02-Mar-15 A | 02-Mar-15 A | |
| L17-9012 | Complete Shower Surrounds | 2 | 1 | 02-Mar-15 A | 13-Apr-15 | 12 |
| LL2-2048 | Set Laundry Room equipment (BY OTHERS) | 1 | 0 | 03-Mar-15 A | 06-Mar-15 A | |
| L1K-8210 | Ceramic tile in restrooms | 7 | 0 | 03-Mar-15 A | 17-Mar-15 A | |
| MPT-1060 | Elevation 33/34 hat channel (east elevation, south er | 3 | 0 | 03-Mar-15 A | 10-Mar-15 A | |
| LL1-8142 | Plumbing fixtures & trim | 2 | 0 | 03-Mar-15 A | 04-Mar-15 A | |
| LL1-Z3-6038 | Paint ceiling at Food Prep (Dry Storage) | 2 | 0 | 03-Mar-15 A | 04-Mar-15 A | |
| L1B-6019 | Frame ceiling clouds | 7 | 0 | 03-Mar-15 A | 06-Mar-15 A | |
| LL1-Z3-8160 | Install doors & hardware at restrooms | 2 | 0 | 03-Mar-15 A | 04-Mar-15 A | |
| L17-9004 | Complete Flooring & Base | 3 | 1 | 03-Mar-15 A | 13-Apr-15 | 14 |
| CO-7116T | Fire Alarm Pre-Testing (Tower) - Tower Levels 4 thru 1( | 6 | 0 | 04-Mar-15 A | 05-Mar-15 A | |
| LL1-8150 | Install bathroom accessories | 2 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L1L-8142 | HVAC drops to 9-wood ceiling - north of Grid K | 2 | 0 | 04-Mar-15 A | 18-Mar-15 A | |
| L1L-8144 | Electrical drops to 9-wood ceiling - north of Grid K | 2 | 0 | 04-Mar-15 A | 18-Mar-15 A | |

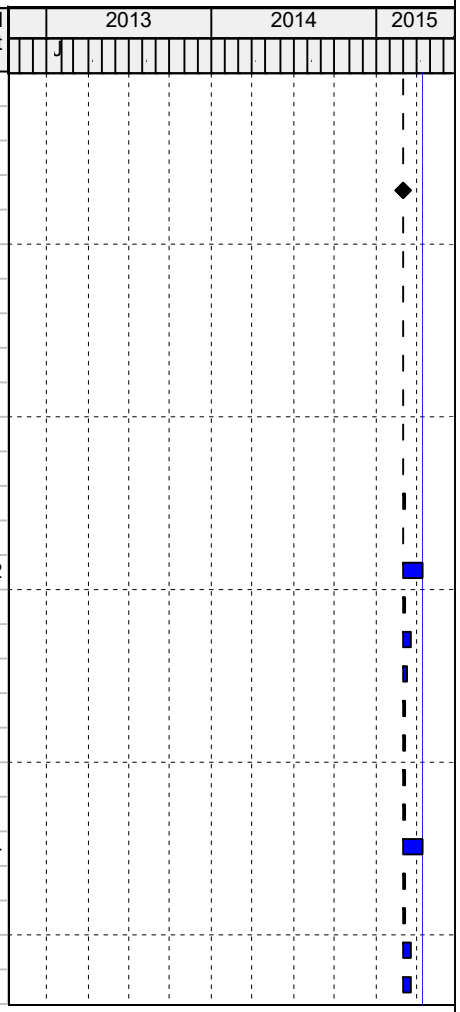



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8146 | Fire sprinkler drops to 9-wood ceiling - north of Grid K | 2 | 0 | 04-Mar-15 A | 18-Mar-15 A | |
| CO-7110T | Fire Sprinkler Pre-Testing (Tower) - Tower Levels 4 thru | 6 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| CO-7110T.1 | Fire Sprinkler Pre-Testing (Tower) - Tower Levels 3, 11 | 2 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| LL1-Z2-8150 | Install base at corridors | 3 | 0 | 05-Mar-15 A | 06-Mar-15 A | |
| L1L-8108 | GWB hang walls & ceilings (Bar) | 2 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L17-9000 | Complete GWB (1714 & 1718) | 5 | 0 | 06-Mar-15 A | 11-Mar-15 A | |
| LL1-Z2-8123 | Floor prep | 1 | 0 | 06-Mar-15 A | 06-Mar-15 A | |
| L1L-8110 | GWB tape & finish walls & ceilings (Bar) | 7 | 0 | 06-Mar-15 A | 12-Mar-15 A | |
| EL-1238 | Elev 1&2 - 30-day correction period | 30 | 0 | 07-Mar-15 A | 10-Apr-15 A | |
| L03-8624 | Fire sprinkler trim at Pool | 2 | 0 | 09-Mar-15 A | 09-Mar-15 A | |
| L11-7032 | Flooring - VCT (x42) | 1 | 0 | 09-Mar-15 A | 09-Mar-15 A | |
| SW-2212 | Zone 2 - FRP sidewalk panels | 3 | 0 | 09-Mar-15 A | 12-Mar-15 A | |
| SW-2048 | Porte Cochere - FRP Porte Cochere drive | 10 | 0 | 09-Mar-15 A | 31-Mar-15 A | |
| L03-8666 | Electrical trim & finish at ceiling at Pool | 2 | 0 | 09-Mar-15 A | 11-Mar-15 A | |
| CO-7139.1 | Install remaining devices & prep devices for testing - | 6 | 0 | 09-Mar-15 A | 12-Mar-15 A | |
| SW-2222 | Zone 2 - Install j-box at NE corner | 1 | 0 | 09-Mar-15 A | 09-Mar-15 A | |
| LL1-Z2-8146 | Floor prep at corridors | 2 | 0 | 09-Mar-15 A | 10-Mar-15 A | |
| L1L-8292 | GWB hang ceilings | 2 | 0 | 09-Mar-15 A | 10-Mar-15 A | |
| CO-7140.1 | Fire Alarm System Device Testing - Tower Levels 4 thr | 6 | 0 | 09-Mar-15 A | 12-Mar-15 A | |
| L1B-6025 | MEP drops at celing clouds (including inspection) | 7 | 0 | 09-Mar-15 A | 18-Mar-15 A | |
| L1L-8230 | Paint, prime & first coat finish | 3 | 0 | 10-Mar-15 A | 10-Mar-15 A | |
| LL2-2100 | Fire sprinkler drops to grid at Laundry | 1 | 0 | 10-Mar-15 A | 10-Mar-15 A | |
| LL1-Z2-8148 | Flooring - carpet at corridors | 3 | 0 | 10-Mar-15 A | 12-Mar-15 A | |
| L1B-8206 | Ceiling grid at West Ballrooms | 3 | 0 | 10-Mar-15 A | 11-Mar-15 A | |
| CM-1024 | Tower - "Clean/Punch" Complete - All Floors [DELETE | 0 | 0 | | 10-Mar-15 A | |
| MPT-1064 | Elevation 33/34 metal panels (east elevation, south e | 7 | 0 | 11-Mar-15 A | 26-Mar-15 A | |
| LL1-Z2-8160 | Flooring - carpet at Jr. Ballroom | 3 | 0 | 11-Mar-15 A | 13-Mar-15 A | |

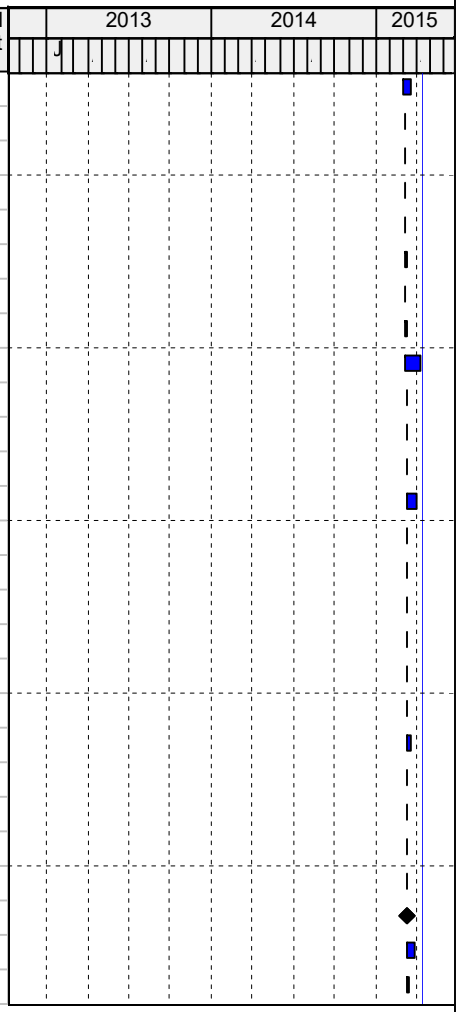



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8258 | GWB tape & finish walls & ceilings | 7 | 0 | 11-Mar-15 A | 17-Mar-15 A | |
| L1BOH2-8120 | Wall coverings - vinyl | 3 | 1 | 12-Mar-15 A | 15-Apr-15 | 5 |
| L1B-8208 | Ceiling grid at East Ballroom | 3 | 0 | 12-Mar-15 A | 13-Mar-15 A | |
| L17-9002 | Complete Painting | 2 | 0 | 12-Mar-15 A | 13-Mar-15 A | |
| L1L-8154 | Paint, prime & first finish coat (Bar) | 2 | 0 | 13-Mar-15 A | 13-Mar-15 A | |
| L1K-8206 | Install toilets at restrooms | 2 | 0 | 16-Mar-15 A | 17-Mar-15 A | |
| MPT-1082 | Caulking - Elevation 48/49 (north elevation, east of 5 | 4 | 0 | 16-Mar-15 A | 19-Mar-15 A | |
| CO-7116T.1 | Smoke Control Equipment Pre-Testing (Fans & Damp | 5 | 0 | 16-Mar-15 A | 20-Mar-15 A | |
| LL1-8128 | Floor prep at Exercise Room | 2 | 0 | 16-Mar-15 A | 16-Mar-15 A | |
| LL1-Z2-8136 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 16-Mar-15 A | 30-Mar-15 A | |
| LL4-8136 | Clear out and clean parking area | 10 | 10 | 16-Mar-15 A | 24-Apr-15 | 10 |
| LL3-8136 | Clear out and clean parking area | 10 | 10 | 16-Mar-15 A | 24-Apr-15 | 10 |
| L1L-8142a | HVAC drops to 9-wood ceiling - south of Grid K | 2 | 0 | 16-Mar-15 A | 16-Mar-15 A | |
| L1L-8144a | Electrical drops to 9-wood ceiling - south of Grid K | 2 | 0 | 16-Mar-15 A | 16-Mar-15 A | |
| L1L-8146a | Fire sprinkler drops to 9-wood ceiling - south of Grid K | 2 | 0 | 16-Mar-15 A | 16-Mar-15 A | |
| L1K-8114a | Celing grid & inspection (west end) | 2 | 0 | 16-Mar-15 A | 19-Mar-15 A | |
| CM-1016c | CM - Owner FF+E "Build-Out" - Floors 6 & 7 | 7 | 0 | 16-Mar-15 A | 22-Mar-15 A | |
| LL2-2118 | Fabricate and deliver washing machine pedestal | 10 | 0 | 16-Mar-15 A | 18-Mar-15 A | |
| I-6902 | RFI 944 - Master control panel | 5 | 0 | 16-Mar-15 A | 03-Apr-15 A | |
| LL1-8138 | Flooring - install cork floor at Exercise Room | 3 | 0 | 17-Mar-15 A | 19-Mar-15 A | |
| LL1-Z3-8206 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 17-Mar-15 A | 23-Mar-15 A | |
| L1L-8302 | Lighting & electrical trim at ceilings | 3 | 0 | 17-Mar-15 A | 18-Mar-15 A | |
| L1K-8120 | Lighting & electrical trim at ceiling | 2 | 0 | 18-Mar-15 A | 19-Mar-15 A | |
| MPP-1020 | Elevation 18/19/21/22 & complete 45 (north elevatior | 12 | 0 | 18-Mar-15 A | 27-Mar-15 A | |
| I-1208 | Paint, prime & first coat finish | 2 | 0 | 18-Mar-15 A | 19-Mar-15 A | |
| L1L-8306 | Fire sprinkler trim | 1 | 0 | 18-Mar-15 A | 18-Mar-15 A | |
| L1L-8128 | Install die wall (Bar) | 3 | 0 | 19-Mar-15 A | 23-Mar-15 A | |

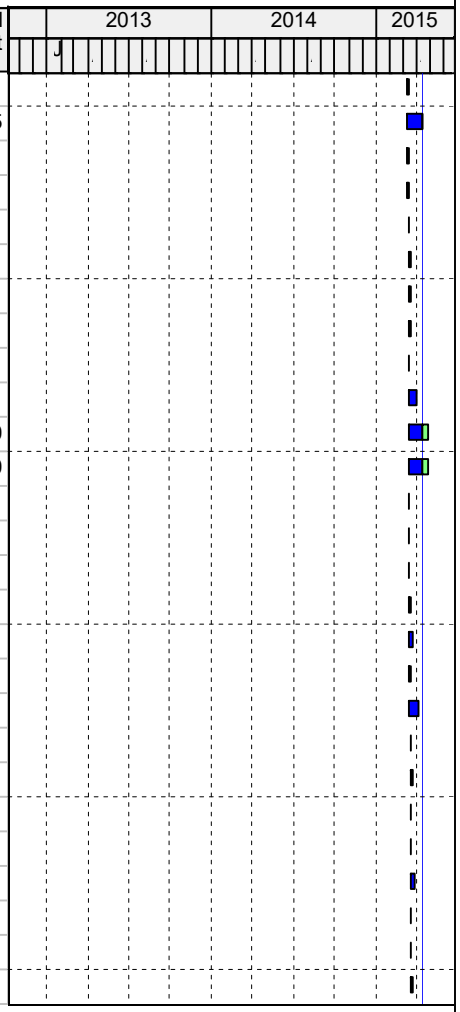



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-6037 | GWB ceiling clouds | 5 | 0 | 19-Mar-15 A | 01-Apr-15 A | |
| LL2-2114 | Install washing machine pedestal | 2 | 0 | 19-Mar-15 A | 20-Mar-15 A | |
| I-5202 | Wall and soffit modifications | 4 | 0 | 19-Mar-15 A | 03-Apr-15 A | |
| LL1-Z3-FCC34 | Paint, final coat & touch-up up at FCC | 2 | 0 | 20-Mar-15 A | 20-Mar-15 A | |
| LL2-2112 | Set washing machines | 1 | 0 | 20-Mar-15 A | 20-Mar-15 A | |
| LL1-Z3-FCC32 | Flooring - VCT at FCC | 2 | 0 | 21-Mar-15 A | 21-Mar-15 A | |
| L1BOH2-8126 | Install doors & hardware | 3 | 0 | 23-Mar-15 A | 31-Mar-15 A | |
| L1K-8128 | Install Kitchen equipment (BY OTHERS) | 5 | 3 | 23-Mar-15 A | 15-Apr-15 | 11 |
| L04-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L05-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L06-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L07-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L08-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L09-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L10-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L02-8130 | Ceiling grid at south half | 3 | 0 | 23-Mar-15 A | 26-Mar-15 A | |
| CO-7226 | Cx - Start-Up - Misc. Equipment | 5 | 0 | 23-Mar-15 A | 27-Mar-15 A | |
| L1BOH2C-6024 | Lighting & electrical trim at ceiling | 2 | 1 | 23-Mar-15 A | 15-Apr-15 | 5 |
| L1L-8136 | Install Peter Glassford art wall | 5 | 0 | 23-Mar-15 A | 27-Mar-15 A | |
| L1L-8282 | Finish carpentry/millwork | 5 | 3 | 23-Mar-15 A | 01-May-15 | 5 |
| LL1-8186a | Wall coverings - complete vinyl at corridors | 2 | 0 | 23-Mar-15 A | 24-Mar-15 A | |
| CM-1016d | CM - Owner FF+E "Build-Out" - Floors 8 & 9 | 7 | 0 | 23-Mar-15 A | 29-Mar-15 A | |
| L02-8184 | Build Kitchen exhaust shaft | 5 | 0 | 23-Mar-15 A | 27-Mar-15 A | |
| L1L-8294 | Ceiling coverings - vinyl | 3 | 0 | 23-Mar-15 A | 25-Mar-15 A | |
| L11-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L12-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L14-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |

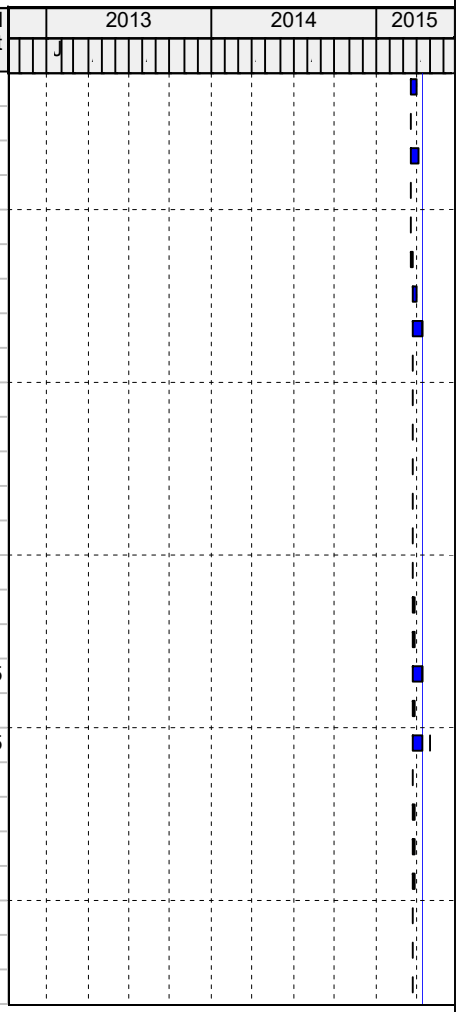


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L16-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L17-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L1K-8122 | Fire sprinkler drops/trim at ceiling | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L1K-8130 | HVAC drops/trim at celing | 2 | 0 | 24-Mar-15 A | 25-Mar-15 A | |
| L1K-8160 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 24-Mar-15 A | 25-Mar-15 A | |
| L17-9016 | Complete Shower Doors | 2 | 1 | 24-Mar-15 A | 15-Apr-15 | 12 |
| I-7010 | RFI 946 - Alterations to bar for epoxy flooring cove | 3 | 0 | 24-Mar-15 A | 30-Mar-15 A | |
| L1L-8310 | Install 9-wood ceiling supports at Sitting Area | 2 | 0 | 25-Mar-15 A | 26-Mar-15 A | |
| L1BOH2-8204 | HVAC drops/trim at ceiling | 2 | 0 | 25-Mar-15 A | 26-Mar-15 A | |
| MPT-1038 | Install louvers, north | 3 | 1 | 25-Mar-15 A | 13-Apr-15 | 17 |
| MPP-1048 | Caulking - Porte Cochere cornice metal | 3 | 0 | 25-Mar-15 A | 27-Mar-15 A | |
| L02-8148 | Paint at Locker Rooms | 2 | 0 | 25-Mar-15 A | 06-Apr-15 A | |
| L1K-8124a2 | Install doors & hardware | 2 | 0 | 25-Mar-15 A | 02-Apr-15 A | |
| L1L-8260 | Wall coverings - vinyl | 2 | 0 | 25-Mar-15 A | 26-Mar-15 A | |
| MPT-1106 | Install alcoves, north | 3 | 1 | 25-Mar-15 A | 13-Apr-15 | 9 |
| MPT-1110 | Cap metal at hi-roof | 3 | 2 | 25-Mar-15 A | 16-Apr-15 | 8 |
| MPT-1118 | Cap metal - Pool terrace | 3 | 2 | 25-Mar-15 A | 21-Apr-15 | 6 |
| L1L-8152 | Install ceiling (Bar) | 3 | 1 | 25-Mar-15 A | 13-Apr-15 | 16 |
| L1L-8116a | Finish carpentry/millwork - south of Grid K | 5 | 2 | 25-Mar-15 A | 14-Apr-15 | 14 |
| LL1-Z2-8142a | Wall coverings - complete vinyl at corridors | 1 | 0 | 25-Mar-15 A | 25-Mar-15 A | |
| L17-9008 | Complete Fire Sprinkler Trim | 1 | 0 | 25-Mar-15 A | 25-Mar-15 A | |
| CO-7222 | Cx - Start-Up - Kitchen Exhaust Fans | 2 | 0 | 26-Mar-15 A | 26-Mar-15 A | |
| L1K-8128a | Kitchen Equipment Final Connections | 10 | 10 | 26-Mar-15 A | 24-Apr-15 | 10 |
| CO-7260 | Cx - Start-Up - Ballroom AAON RTU | 1 | 0 | 26-Mar-15 A | 26-Mar-15 A | |
| L1L-8148 | Electrical rough-in at die wall (Bar) | 4 | 0 | 26-Mar-15 A | 31-Mar-15 A | |
| L17-9006 | Complete Lighting & Electrical Trim | 2 | 0 | 26-Mar-15 A | 31-Mar-15 A | |

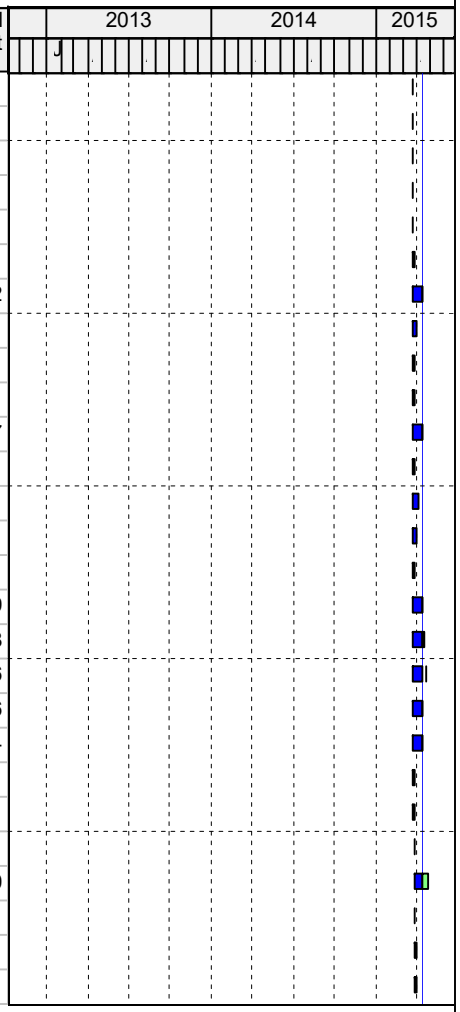



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-5084 | Zone 3 - FRP door apron at SE corner | 2 | 0 | 26-Mar-15 A | 27-Mar-15 A | |
| LL2-2116 | Relocate dryers and remove floor coping at dryer area | 3 | 0 | 26-Mar-15 A | 27-Mar-15 A | |
| L1B-8176 | Complete shaft wall at Prefunction 1 south end | 4 | 0 | 26-Mar-15 A | 02-Apr-15 A | |
| L1L-8206 | Lighting & electrical trim at ceilings - north of Grid K | 2 | 0 | 26-Mar-15 A | 31-Mar-15 A | |
| LL1-Z3-8128 | Flooring - VCT | 5 | 0 | 27-Mar-15 A | 10-Apr-15 A | |
| L1L-8312 | HVAC drops to 9-wood ceiling | 2 | 0 | 27-Mar-15 A | 02-Apr-15 A | |
| L1L-8314 | Electrical drops to 9-wood ceiling | 2 | 0 | 27-Mar-15 A | 02-Apr-15 A | |
| L1L-8316 | Fire sprinkler drops to 9-wood ceiling | 2 | 0 | 27-Mar-15 A | 02-Apr-15 A | |
| L1L-8150 | Plumbing rough-in at die wall (Bar) | 4 | 0 | 27-Mar-15 A | 31-Mar-15 A | |
| CN-1000 | Install exterior canopies - steel | 5 | 0 | 27-Mar-15 A | 01-Apr-15 A | |
| L03-8682 | Install waterproofing and protection layer | 3 | 0 | 27-Mar-15 A | 02-Apr-15 A | |
| L1B-8174 | Complete grease duct insulation & inspect at Prefunc | 5 | 5 | 27-Mar-15 A | 17-Apr-15 | 0 |
| L17-7046 | Field mesaure and fabricate vending countertops (OF | 10 | 5 | 27-Mar-15 A | 20-Apr-15 | 20 |
| CO-7230 | Cx - TAB - Air Balancing - Tower | 15 | 0 | 30-Mar-15 A | 10-Apr-15 A | |
| CO-7141 | Install Fire Alarm Devices & Map to Panel - Podium | 5 | 5 | 30-Mar-15 A | 17-Apr-15 | 0 |
| MPT-1094 | Caulking - Elevation 32 (south elevation, east of man | 10 | 0 | 30-Mar-15 A | 10-Apr-15 A | |
| MPT-1096 | Caulking - Elevation 33/34 (east elevation, south end | 10 | 0 | 30-Mar-15 A | 10-Apr-15 A | |
| I-6012 | Core drill & install new floor drain and piping | 2 | 0 | 30-Mar-15 A | 31-Mar-15 A | |
| CM-1016b | CM - Owner FF&E "Build-Out" - Floors 10 & 11 | 7 | 0 | 30-Mar-15 A | 05-Apr-15 A | |
| LL2-2110 | Restore epoxy flooring at dryer location | 5 | 0 | 30-Mar-15 A | 03-Apr-15 A | |
| I-1204 | Finish carpentry/millwork at Concierge Lounge | 5 | 0 | 31-Mar-15 A | 07-Apr-15 A | |
| LL1-8130 | Install base | 3 | 0 | 31-Mar-15 A | 03-Apr-15 A | |
| L1L-8138 | Flooring - epoxy floor (Bar) | 5 | 0 | 31-Mar-15 A | 03-Apr-15 A | |
| L1L-8280 | Install Peter Glassford art wall | 5 | 0 | 31-Mar-15 A | 03-Apr-15 A | |
| LL1-Z2-8144 | Install doors & hardware at corridors | 2 | 0 | 31-Mar-15 A | 01-Apr-15 A | |
| L1K-8212 | Lighting & electrical trim at ceiling | 2 | 0 | 31-Mar-15 A | 01-Apr-15 A | |
| L1L-8304 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 31-Mar-15 A | 31-Mar-15 A | |

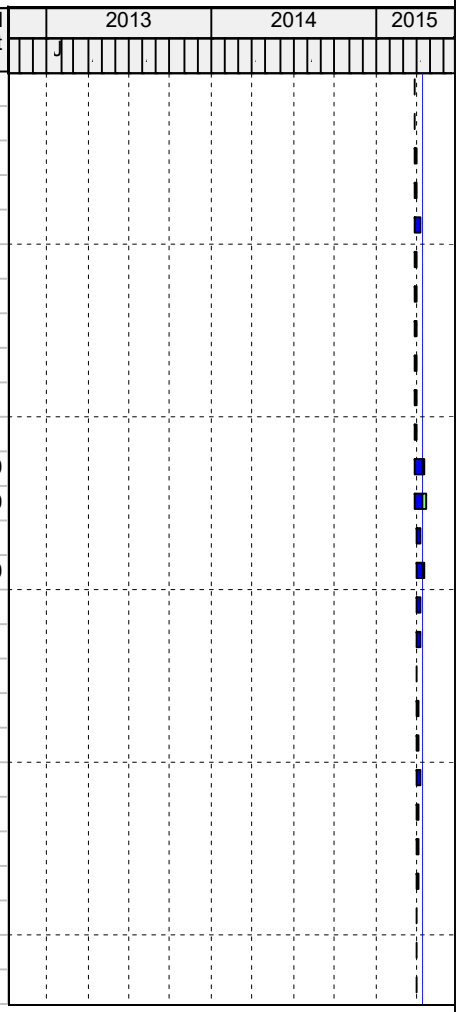



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8669 | Install anchor bolts for trench drain | 1 | 0 | 31-Mar-15 A | 31-Mar-15 A | |
| L1B-8178 | Complete framing & MEP at Prefunction 1 south end | 3 | 0 | 31-Mar-15 A | 02-Apr-15 A | |
| CO-7102T | Cx - DDC Point-To-Point - Central Plant [DELETED] | 5 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7132 | Cx - DDC Point-To-Point - Ballroom VAV [DELETED] | 4 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7134 | Cx - DDC Point-To-Point - Ballroom RTU (2) [DELETEI | 2 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7402 | Cx - FPT - Central Plant [DELETED] | 2 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7406 | Cx - FPT - MUA, RTU, VAV and Exhaust Fansm [DEL | 5 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7408 | Cx - FPT - Garage Exhaust Fans [DELETED] | 1 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7410 | Cx - FPT - Misc Equipment [DELETED] | 4 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| MPP-1004 | Pool Area cornice metal | 10 | 5 | 01-Apr-15 A | 17-Apr-15 | 5 |
| L03-8622 | HVAC trim at Pool | 2 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| LL2-2102 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 01-Apr-15 A | 06-Apr-15 A | |
| L1BOH2C-6026 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 1 | 01-Apr-15 A | 15-Apr-15 | 5 |
| L1L-8140a | Install 9-wood ceiling - south of Grid K | 4 | 0 | 01-Apr-15 A | 06-Apr-15 A | |
| CO-7116.1 | Smoke Control Equipment Pre-Testing (Fans & Dampr | 18 | 10 | 01-Apr-15 A | 24-Apr-15 | 0 |
| L02-8158 | Ceiling grid at north half | 3 | 2 | 02-Apr-15 A | 14-Apr-15 | 1 |
| L03-8206a | Flooring - carpet at corridors (E-W leg) | 2 | 0 | 02-Apr-15 A | 03-Apr-15 A | |
| I-6014 | Install temporary partition at corridor | 1 | 0 | 02-Apr-15 A | 02-Apr-15 A | |
| L1L-8320 | Paint, above 9-wood ceiling | 2 | 0 | 03-Apr-15 A | 06-Apr-15 A | |
| L1BOH2-8116 | Finish carpentry/millwork | 5 | 0 | 06-Apr-15 A | 06-Apr-15 A | |
| LL1-Z3-FCC38 | Final clean and punch list at FCC | 3 | 0 | 06-Apr-15 A | 07-Apr-15 A | |
| MPT-1074 | Tower Sign, South (El 32) | 5 | 0 | 06-Apr-15 A | 08-Apr-15 A | |
| L1L-8130 | Install bar and back bar | 10 | 5 | 06-Apr-15 A | 17-Apr-15 | 15 |
| L1L-8232 | Wall coverings - vinyl | 5 | 1 | 06-Apr-15 A | 13-Apr-15 | 3 |
| L1B-8142 | Paint, prime & first coat finish walls & ceilings at corrid | 2 | 0 | 06-Apr-15 A | 10-Apr-15 A | |
| L1B-8162 | Install doors & hardware at corridors | 2 | 0 | 06-Apr-15 A | 07-Apr-15 A | |
| L1L-8206a | Lighting & elecrical trim at ceilings - south of Grid K | 2 | 0 | 06-Apr-15 A | 06-Apr-15 A | |

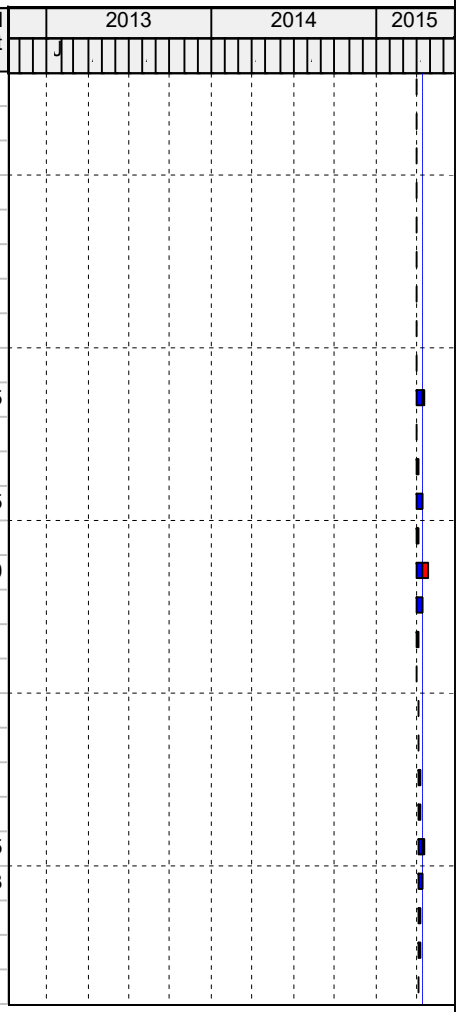



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CM-1016e | CM - Owner FF+E "Build-Out" - Floors 12 & 14 | 7 | 0 | 06-Apr-15 A | 12-Apr-15 A | |
| SW-2050 | Street - Grind and overlay | 5 | 0 | 06-Apr-15 A | 09-Apr-15 A | |
| CN-1004 | Field measure & fabricate canopy glass | 15 | 10 | 06-Apr-15 A | 24-Apr-15 | 8 |
| CO-7139.2 | Install Fire Alarm Devices & Map to Panel - Tower Lev | 2 | 0 | 06-Apr-15 A | 08-Apr-15 A | |
| I-7100 | Resolve dryer duct issue | 10 | 10 | 06-Apr-15 A | 24-Apr-15 | 7 |
| I-7102 | TPAP box impact | 5 | 5 | 06-Apr-15 A | 17-Apr-15 | 3 |
| L03-8628 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L02-8140 | Lighting & electrical trim at south half | 2 | 1 | 07-Apr-15 A | 15-Apr-15 | 2 |
| L1L-8234 | Fire sprinkler trim at ceilings | 1 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8236 | Lighting & electrical trim at ceilings | 2 | 1 | 07-Apr-15 A | 14-Apr-15 | 10 |
| L1L-8262 | Fire sprinkler trim at ceilings | 1 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8264 | Lighting & electrical trim at ceilings | 3 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8266 | HVAC drops/trim at celing | 2 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8284 | Install handrails | 2 | 0 | 07-Apr-15 A | 08-Apr-15 A | |
| L1L-8298 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8318 | Install 9-wood ceiling at Sitting Area | 3 | 1 | 07-Apr-15 A | 13-Apr-15 | 10 |
| L1L-8204a | HVAC trim at ceiling - south of Grid K | 1 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8112a | Fire sprinkler trim - south of Grid K | 1 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| I-1206 | Install ceiling at Concierge Lounge (BOK) | 4 | 0 | 08-Apr-15 A | 09-Apr-15 A | |
| L1L-8238 | HVAC drops/trim at celing | 1 | 0 | 08-Apr-15 A | 08-Apr-15 A | |
| LL1-8152 | Measure & fabricate mirrors | 10 | 10 | 09-Apr-15 A | 24-Apr-15 | 7 |
| L1K-8128b | Ansul system final connections | 10 | 10 | 10-Apr-15 A | 24-Apr-15 | 10 |
| L17-7032 | Flooring - VCT (x42) | 1 | 1 | 13-Apr-15 | 13-Apr-15 | 14 |
| L1B-8128 | Install base at Ballrooms | 5 | 5 | 13-Apr-15 | 17-Apr-15 | 8 |
| SW-2122 | Zone 1 - Install landscaping & irrigation | 15 | 15 | 13-Apr-15 | 01-May-15 | 8 |
| SW-2218 | Zone 2 - Install landscaping & irrigation | 15 | 15 | 13-Apr-15 | 01-May-15 | 8 |
| L17-8140 | Complete window sills | 1 | 1 | 13-Apr-15 | 13-Apr-15 | 14 |

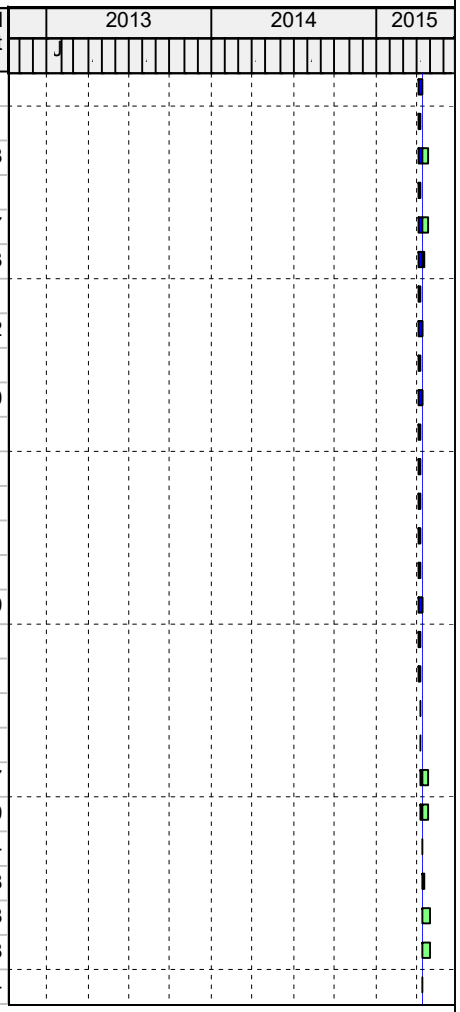


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7264 | Cx - Start-Up - Lobby Trane TRU (2) | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 44 |
| CO-7136 | Cx - DDC Point-To-Point | 10 | 10 | 13-Apr-15 | 24-Apr-15 | 5 |
| L03-8672 | Prep & pour pool topping slab | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 1 |
| LL1-Z3-FCC40 | Install Knox Box at FCC | 1 | 1 | 13-Apr-15 | 13-Apr-15 | 15 |
| CO-7138 | Elevator Finals with AHJ | 12 | 12 | 13-Apr-15 | 28-Apr-15 | 16 |
| L02-8142 | Ceiling grid at Locker Rooms | 3 | 3 | 13-Apr-15 | 15-Apr-15 | 7 |
| L02-8150 | Install doors & hardware at Locker Rooms | 1 | 1 | 13-Apr-15 | 13-Apr-15 | 14 |
| L1K-8202 | Ceiling grid at Janitorial | 1 | 1 | 13-Apr-15 | 13-Apr-15 | 8 |
| L1L-8239 | Floor prep | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 6 |
| I-1210 | Floor prep | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 9 |
| SW-2330 | Zone 3 - Landscaping & irrigation | 15 | 15 | 13-Apr-15 | 01-May-15 | 8 |
| L1L-8308 | Floor (stair) prep | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 8 |
| L02-8154 | Wall coverings - vinyl at north half | 3 | 3 | 13-Apr-15 | 15-Apr-15 | 1 |
| MPP-1018 | Elevation A/B/C (Porte Cochere wall panels) | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 9 |
| MPP-1060 | Install alcoves, south | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 16 |
| MPP-1064 | Install column at Pool | 1 | 1 | 13-Apr-15 | 13-Apr-15 | 5 |
| LL2-8152 | Clear out and clean parking area | 10 | 10 | 13-Apr-15* | 24-Apr-15 | 4 |
| LL1-Z3-8158 | Install toilet partitions | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 14 |
| CO-7154 | Final Inspection - Mechanical | 5 | 5 | 13-Apr-15 | 17-Apr-15 | 23 |
| L1L-8118a | Fire alarm trim (spreaker strobe & smoke detector bas | 1 | 1 | 13-Apr-15 | 13-Apr-15 | 15 |
| MPT-1120 | Cap metal at L12 Terrace | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 8 |
| LL2-8156 | Remove job shacks | 1 | 1 | 13-Apr-15 | 13-Apr-15 | 14 |
| CM-1016f | CM - Owner FF+E "Build-Out" - Floors 15 & 16 | 7 | 7 | 13-Apr-15 | 19-Apr-15 | 10 |
| CO-7231 | Cx - TAB - Air Balancing - Podium | 10 | 10 | 13-Apr-15 | 24-Apr-15 | 0 |
| CO-7104T.3 | Compile/Certify/Accept TAB Report - Tower | 3 | 3 | 13-Apr-15 | 15-Apr-15 | 3 |
| I-7000 | Owner post bond for site lighting for TCO | 0 | 0 | | 13-Apr-15 | 23 |
| L03-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 1 | 14-Apr-15* | 14-Apr-15 | 14 |

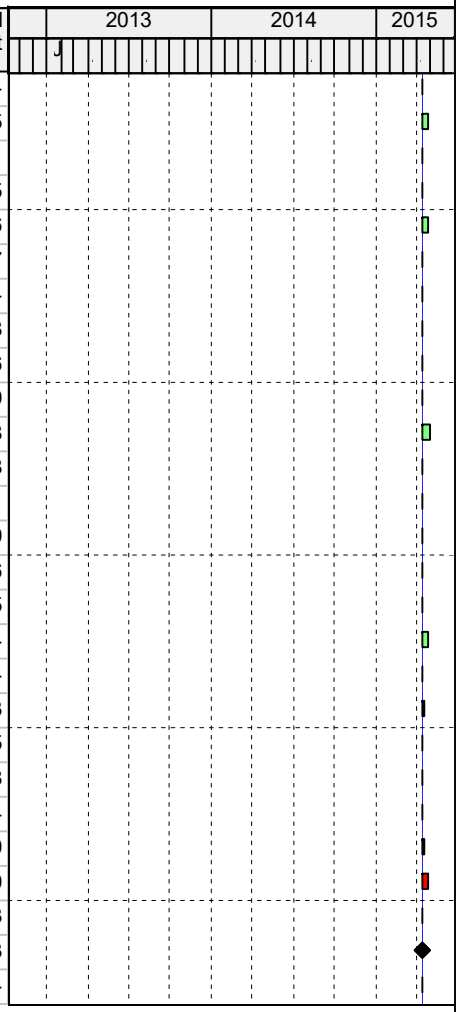



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-FCC22 | Final inspections by CoB and Fire Marshall | 2 | 2 | 14-Apr-15 | 15-Apr-15 | 15 |
| MPP-1038 | Podium Signs, West | 5 | 5 | 14-Apr-15 | 20-Apr-15 | 12 |
| LL1-Z3-8152 | Complete MEP trim | 2 | 2 | 14-Apr-15 | 15-Apr-15 | 15 |
| L1L-8242 | Finish carpentry/millwork (including front desk) | 4 | 4 | 14-Apr-15 | 17-Apr-15 | 3 |
| LL2-8106b | Pinned insulation at ramp at Garage & dry shack area | 5 | 5 | 14-Apr-15 | 20-Apr-15 | 14 |
| L1L-8286 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 14-Apr-15 | 15-Apr-15 | 10 |
| I-1202 | Flooring - tile & carpet at Concierge Lounge | 7 | 7 | 15-Apr-15 | 23-Apr-15 | 9 |
| L03-8630 | Install doors & hardware at Pool | 2 | 2 | 15-Apr-15 | 16-Apr-15 | 21 |
| L03-8670 | Installl trench drains at Pool | 2 | 2 | 15-Apr-15 | 16-Apr-15 | 1 |
| CO-7104T.1 | Fire Alarm/Smoke Control Pre-Functional Testing - To | 10 | 10 | 15-Apr-15 | 28-Apr-15 | 3 |
| LL1-Z3-8150 | Complete paint final coat & touch-up | 2 | 2 | 15-Apr-15 | 16-Apr-15 | 14 |
| LL1-Z3-8154 | Complete MEP trim | 2 | 2 | 15-Apr-15 | 16-Apr-15 | 14 |
| L1B-8146 | HVAC drops/trim at corridors | 2 | 2 | 15-Apr-15 | 16-Apr-15 | 8 |
| L1L-8203 | Complete MEP trim | 2 | 2 | 15-Apr-15 | 16-Apr-15 | 16 |
| L02-8160 | HVAC drops/trim at north half | 2 | 2 | 15-Apr-15 | 16-Apr-15 | 1 |
| L02-8166 | Fire sprinkler trim at north half | 2 | 2 | 15-Apr-15 | 16-Apr-15 | 3 |
| MPP-1050 | Columns at Porte Cochere | 4 | 4 | 15-Apr-15 | 20-Apr-15 | 9 |
| L1K-8222 | Install toilet partitions | 2 | 2 | 15-Apr-15 | 16-Apr-15 | 14 |
| SW-2068 | Street - Striping | 2 | 2 | 15-Apr-15* | 16-Apr-15 | 17 |
| L1BOH2-8112 | Fire sprinkler drops/trim at ceiling | 1 | 1 | 16-Apr-15 | 16-Apr-15 | 8 |
| L1L-8120 | Plumbing fixtures & trim (Bar) | 2 | 2 | 16-Apr-15 | 17-Apr-15 | 15 |
| L1L-8122 | Electrical trim & finish at bar (bar area final connectior | 2 | 2 | 16-Apr-15 | 17-Apr-15 | 15 |
| L1L-8124a | Install base | 3 | 3 | 16-Apr-15 | 20-Apr-15 | 14 |
| L02-8145 | MEP drops to framed ceiling (including inspections) | 2 | 2 | 16-Apr-15 | 17-Apr-15 | 7 |
| L1BOH2-8123 | Floor prep | 2 | 2 | 16-Apr-15 | 17-Apr-15 | 5 |
| L1L-8123 | Floor prep - north of Grid K | 2 | 2 | 16-Apr-15* | 17-Apr-15 | 7 |
| L1B-8144 | Wall coverings - vinyl at corridors | 3 | 3 | 16-Apr-15 | 20-Apr-15 | 7 |

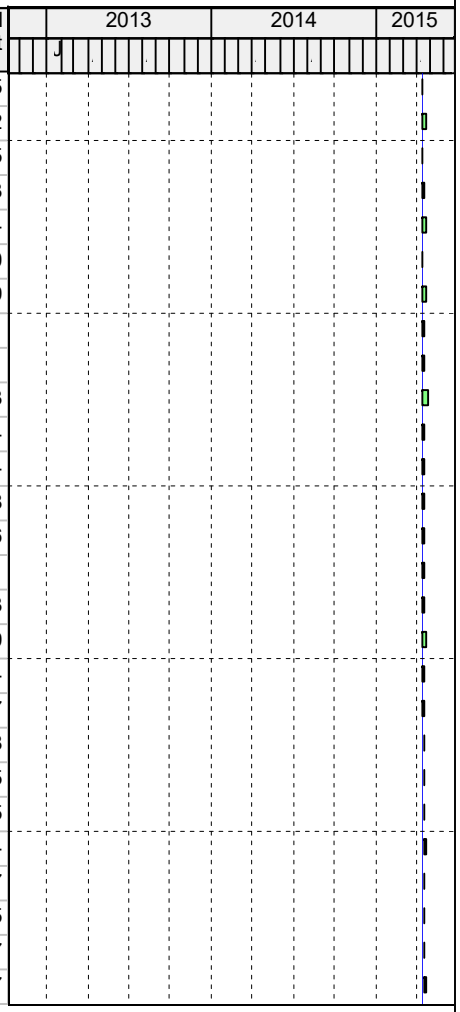



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-8148 | Lighting & electrical trim at corridors | 2 | 2 | 16-Apr-15 | 17-Apr-15 | 8 |
| L1B-8150 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 16-Apr-15 | 17-Apr-15 | 9 |
| L1B-8156 | Install base at corridors | 5 | 5 | 16-Apr-15 | 22-Apr-15 | 7 |
| L02-8156 | Install doors & hardware at north half | 3 | 3 | 16-Apr-15 | 20-Apr-15 | 1 |
| L1L-8123a | Floor prep - south of Grid K | 2 | 2 | 16-Apr-15 | 17-Apr-15 | 11 |
| LL1-Z3-8136 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 16-Apr-15 | 22-Apr-15 | 15 |
| MPT-1084 | Caulking - Hi-roof cornice metal | 6 | 6 | 17-Apr-15 | 24-Apr-15 | 8 |
| L02-8114 | Floor prep at south half | 2 | 2 | 17-Apr-15 | 20-Apr-15 | 1 |
| L02-8162 | Lighting & electrical trim at north half | 2 | 2 | 17-Apr-15 | 20-Apr-15 | 1 |
| L02-8164 | Fire alarm trim (speaker/strobe & smoke detector bas | 2 | 2 | 17-Apr-15 | 20-Apr-15 | 1 |
| L03-8674 | Install storefront at Pool entry | 2 | 2 | 17-Apr-15 | 20-Apr-15 | 1 |
| SW-2070 | Street - Signage | 2 | 2 | 17-Apr-15 | 20-Apr-15 | 17 |
| L03-8688 | Complete pool topping slab | 2 | 2 | 17-Apr-15 | 20-Apr-15 | 1 |
| L1BOH2-8124 | Flooring - VCT | 3 | 3 | 20-Apr-15 | 22-Apr-15 | 7 |
| CM-1016a | CM - Owner FF+E "Build-Out" - Floors 3 & 17 | 7 | 7 | 20-Apr-15 | 26-Apr-15 | 10 |
| MPP-1040 | Caulking - Pool Area & Ballroom cornice metal | 8 | 8 | 20-Apr-15 | 29-Apr-15 | 5 |
| L1BOH2-8128 | Flooring - carpet | 3 | 3 | 20-Apr-15 | 22-Apr-15 | 5 |
| L1B-8202 | Wall coverings - vinyl at Ballrooms | 5 | 5 | 20-Apr-15 | 24-Apr-15 | 3 |
| L1L-8240 | Flooring - tile & base | 10 | 10 | 20-Apr-15 | 01-May-15 | 3 |
| L1L-8278 | Flooring - tile at stair treads | 10 | 10 | 20-Apr-15 | 01-May-15 | 5 |
| L1B-8129 | Floor prep | 2 | 2 | 20-Apr-15 | 21-Apr-15 | 6 |
| L1B-8152 | Fire sprinkler drops/trim at corridors | 1 | 1 | 20-Apr-15 | 20-Apr-15 | 9 |
| L1B-8160 | Floor prep | 2 | 2 | 20-Apr-15 | 21-Apr-15 | 8 |
| L02-8168 | Floor prep at north half | 1 | 1 | 20-Apr-15 | 20-Apr-15 | 1 |
| LL1-Z3-8156 | Install countertops at restrooms | 2 | 2 | 20-Apr-15 | 21-Apr-15 | 7 |
| CO-7152 | Final Inspection - Plumbing | 5 | 5 | 20-Apr-15 | 24-Apr-15 | 18 |
| LL1-8116a | Install countertops (owner-furnished) | 2 | 2 | 20-Apr-15 | 21-Apr-15 | 13 |

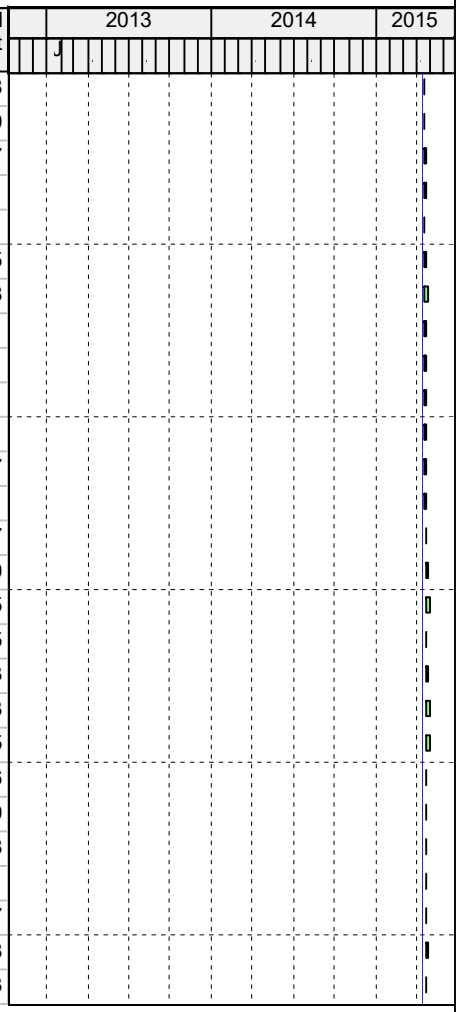



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-8116a | Install countertops (owner-furnished) | 1 | 1 | 20-Apr-15 | 20-Apr-15 | 12 |
| L1B-8154 | Finish carpentry/millwork at corridors | 2 | 2 | 21-Apr-15 | 22-Apr-15 | 7 |
| L02-8152 | Flooring - VCT at south half | 10 | 10 | 21-Apr-15 | 04-May-15 | 1 |
| L02-8170 | Flooring - VCT at north half | 10 | 10 | 21-Apr-15 | 04-May-15 | 1 |
| MPP-1056 | Caulking - Porte Cochere walls & columns | 3 | 3 | 21-Apr-15 | 23-Apr-15 | 9 |
| CO-7144 | Final Inspection - Transportation (Right-Of-Way) | 5 | 5 | 21-Apr-15 | 27-Apr-15 | 17 |
| CO-7148 | Final Inspection - Utilities | 5 | 5 | 21-Apr-15 | 27-Apr-15 | 17 |
| L17-7048 | Install vending countertops (OFM) - L4-L17 | 2 | 2 | 21-Apr-15 | 22-Apr-15 | 20 |
| L1K-8220 | Install countertops in restrooms | 2 | 2 | 22-Apr-15 | 23-Apr-15 | 7 |
| LL1-Z3-8162 | Install sinks at Restrooms | 2 | 2 | 22-Apr-15 | 23-Apr-15 | 7 |
| L1K-8342 | Final connections at walk-in cooler/freezer | 2 | 2 | 23-Apr-15 | 24-Apr-15 | 10 |
| L1BOH2-8124a | Install base | 5 | 5 | 23-Apr-15 | 29-Apr-15 | 5 |
| L1B-8130 | Flooring - VCT at service corridor and A/V room | 3 | 3 | 23-Apr-15 | 27-Apr-15 | 7 |
| LL1-Z3-8146 | Install restroom accessories | 2 | 2 | 24-Apr-15 | 27-Apr-15 | 7 |
| L1L-8268 | Complete MEP trim | 2 | 2 | 24-Apr-15 | 27-Apr-15 | 9 |
| L1L-8300 | Paint, final coat & touch-up | 2 | 2 | 24-Apr-15 | 27-Apr-15 | 9 |
| L1L-8124b | Flooring - wood - south of Grid K | 4 | 4 | 24-Apr-15 | 29-Apr-15 | 7 |
| L1K-8224 | Install sinks at restrooms | 2 | 2 | 24-Apr-15 | 27-Apr-15 | 7 |
| CO-7172 | Compile/Certify/Accept TAB Report - Podium | 3 | 3 | 24-Apr-15 | 28-Apr-15 | 0 |
| LL2-2050 | Laundry Room equipment final connections (MEP) | 3 | 3 | 27-Apr-15 | 29-Apr-15 | 7 |
| RF-4066 | Pool Green Roof - Install decorative metal railing | 5 | 5 | 27-Apr-15* | 01-May-15 | 3 |
| LL2-8144 | Complete acoustical ceiling tile | 2 | 2 | 27-Apr-15 | 28-Apr-15 | 8 |
| LL1-8144 | Install mirrors | 3 | 3 | 27-Apr-15 | 29-Apr-15 | 7 |
| CN-1002 | Install exterior canopies - glass | 5 | 5 | 27-Apr-15 | 01-May-15 | 8 |
| LL4-8138 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 27-Apr-15 | 01-May-15 | 10 |
| LL3-8138 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 27-Apr-15 | 01-May-15 | 10 |
| EL-1240 | Elev 1&2 - Final elevator inspection | 2 | 2 | 27-Apr-15 | 28-Apr-15 | 34 |

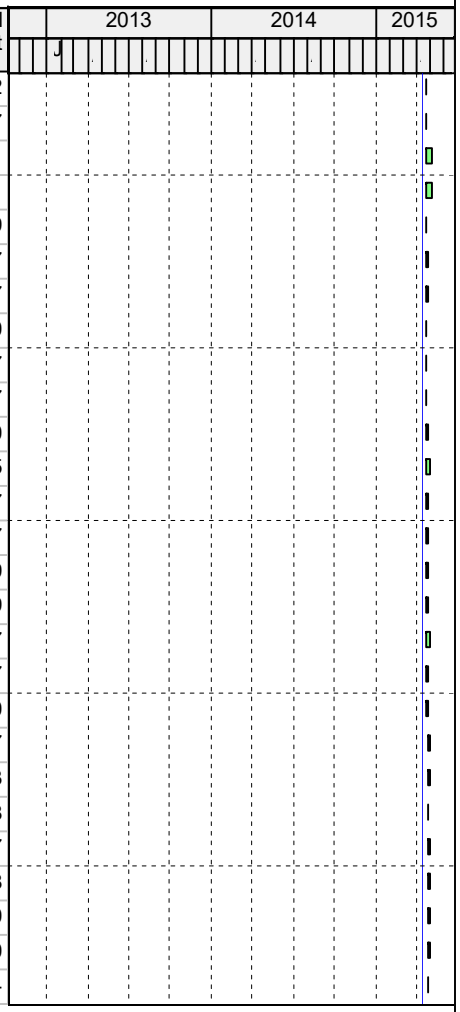



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8640 | Prep and install pool plaster | 3 | 3 | 28-Apr-15 | 30-Apr-15 | 1 |
| L1K-8208 | Install restroom accessories | 2 | 2 | 28-Apr-15 | 29-Apr-15 | 7 |
| LL1-8146 | Complete MEP trim | 2 | 2 | 28-Apr-15 | 29-Apr-15 | 7 |
| LL1-8148 | Complete acoustical ceiling tile | 2 | 2 | 28-Apr-15 | 29-Apr-15 | 7 |
| LL1-8188 | Complete paint final coat & touch-up | 2 | 2 | 28-Apr-15 | 29-Apr-15 | 7 |
| L02-8172 | Finish carpentry/millwork at north half | 1 | 1 | 28-Apr-15 | 28-Apr-15 | 6 |
| LL1-Z2-8162 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 28-Apr-15 | 04-May-15 | 7 |
| L1B-8158 | Flooring - carpet at corridors | 3 | 3 | 29-Apr-15 | 01-May-15 | 3 |
| L1BOH2-8140 | Acoustical ceiling tile | 2 | 2 | 30-Apr-15 | 01-May-15 | 5 |
| L1BOH2-8201 | Paint, final coat & touch-up | 2 | 2 | 30-Apr-15 | 01-May-15 | 5 |
| L1BOH2-8118 | Complete MEP trim | 2 | 2 | 30-Apr-15 | 01-May-15 | 5 |
| CO-7160 | Generator - Cx generator/owner training | 3 | 3 | 30-Apr-15 | 04-May-15 | 14 |
| LL1-8190 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 30-Apr-15 | 06-May-15 | 7 |
| L03-8618 | Ceramic tile at pool area | 8 | 8 | 01-May-15 | 12-May-15 | 1 |
| L03-8642 | Fill pool | 1 | 1 | 01-May-15 | 01-May-15 | 2 |
| L03-8644 | Connect, startup & adjust pool equipment | 10 | 10 | 04-May-15 | 15-May-15 | 2 |
| L02-8138 | Complete acoustical ceiling tile | 2 | 2 | 04-May-15 | 05-May-15 | 3 |
| RF-4068 | Pool Green Roof - Install American Hydrotech assem | 3 | 3 | 04-May-15 | 06-May-15 | 5 |
| RF-4070 | TR - Terrace Roof - Install American Hydrotech assem | 3 | 3 | 04-May-15 | 06-May-15 | 5 |
| L1B-8136 | Complete MEP trim | 2 | 2 | 04-May-15 | 05-May-15 | 3 |
| L1K-8154 | Complete acoustical ceiling tile | 2 | 2 | 04-May-15 | 05-May-15 | 3 |
| L1K-8156 | Complete MEP trim | 2 | 2 | 04-May-15 | 05-May-15 | 3 |
| L1K-8158 | Complete paint final coat & touch-up | 2 | 2 | 04-May-15 | 05-May-15 | 3 |
| L1L-8244 | Complete MEP trim | 2 | 2 | 04-May-15 | 05-May-15 | 3 |
| L1K-8125 | Floor prep | 1 | 1 | 04-May-15 | 04-May-15 | 1 |
| L1L-8288 | Paint, final coat & touch-up | 2 | 2 | 04-May-15 | 05-May-15 | 3 |
| CO-7146 | Final Inspection - Clear & Grade | 5 | 5 | 04-May-15 | 08-May-15 | 8 |

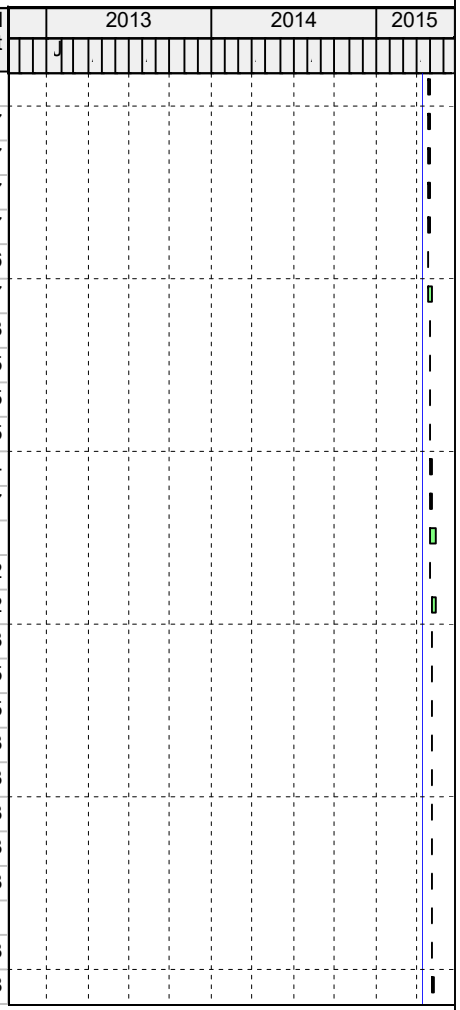



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7500 | Complete Final Walsh/WPM Inspections/Corrections | 10 | 10 | 04-May-15 | 15-May-15 | 3 |
| L1BOH2-8136 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 04-May-15 | 08-May-15 | 5 |
| L1B-8168 | Wall coverings - vinyl at Prefunction 2 | 2 | 2 | 04-May-15 | 05-May-15 | 0 |
| L1B-8180 | HVAC drops/trim at Prefunction 2 | 2 | 2 | 04-May-15 | 05-May-15 | 1 |
| L1B-8182 | Lighting & electrical trim at Prefunction 2 | 2 | 2 | 04-May-15 | 05-May-15 | 1 |
| L1B-8184 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 04-May-15 | 05-May-15 | 1 |
| CO-7156 | Final Inspection - Health Department (Kitchens) | 5 | 5 | 05-May-15 | 11-May-15 | 7 |
| LL2-8154 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 05-May-15 | 11-May-15 | 4 |
| CO-7150 | Final Inspection - Electrical | 5 | 5 | 06-May-15 | 12-May-15 | 6 |
| L1K-8166 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 06-May-15 | 12-May-15 | 3 |
| L1L-8156 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 06-May-15 | 12-May-15 | 3 |
| L02-8182 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 06-May-15 | 12-May-15 | 3 |
| L1B-8186 | Fire sprinkler drops/trim at Prefunction 2 | 1 | 1 | 06-May-15 | 06-May-15 | 1 |
| L1B-8188 | Finish carpentry/millwork at Prefunction 2 | 2 | 2 | 06-May-15 | 07-May-15 | 0 |
| L1B-8190 | Install base at Prefunction 2 | 2 | 2 | 06-May-15 | 07-May-15 | 0 |
| L1B-8194 | Floor prep at Prefunction 2 | 1 | 1 | 06-May-15 | 06-May-15 | 1 |
| L1B-8192 | Flooring - carpet at Prefunction 2 | 2 | 2 | 08-May-15 | 11-May-15 | 0 |
| L1BOH2-8134 | Final Cleaning | 2 | 2 | 11-May-15 | 12-May-15 | 5 |
| L1B-8172 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 11-May-15 | 15-May-15 | 0 |
| L1BOH2-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 13-May-15 | 15-May-15 | 5 |
| L03-8620 | Plumbing fixtures & trim at Pool | 2 | 2 | 13-May-15 | 14-May-15 | 1 |
| L03-8626 | Electrical trim & finish at Pool | 2 | 2 | 13-May-15 | 14-May-15 | 1 |
| L03-8638 | Install pool deck and ADA lift | 3 | 3 | 13-May-15 | 15-May-15 | 2 |
| L03-8632 | Install restroom accessories at Pool | 2 | 2 | 15-May-15 | 18-May-15 | 1 |
| L1BOH2-81214 | L1, Zone 3 Complete | 0 | 0 | | 15-May-15 | 5 |
| LL2-8150 | LL2 Floor Complete | 0 | 0 | | 18-May-15 | 4 |
| L03-8646 | Health inspection | 1 | 1 | 19-May-15 | 19-May-15 | 1 |

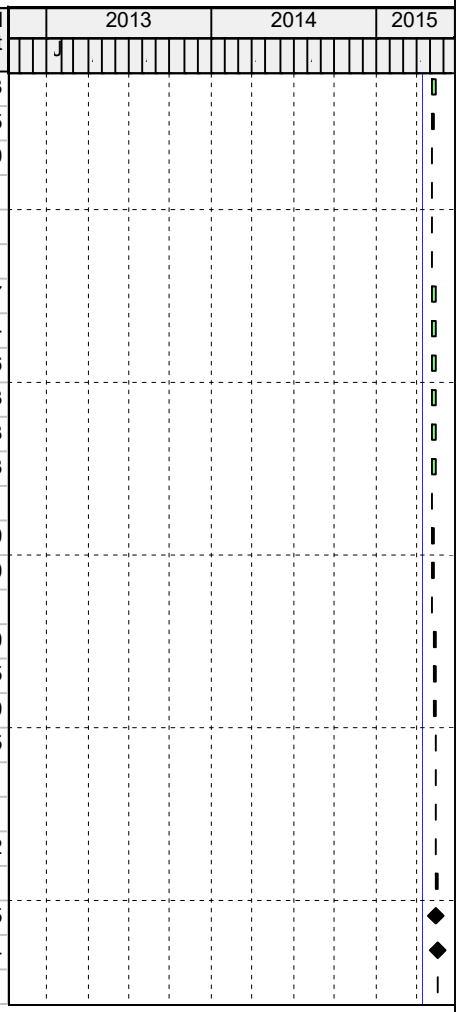



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8676 | Contractor Punchlist at Pool (inspect/distribute/correct | 5 | 5 | 20-May-15 | 27-May-15 | 4 |
| CO-7124 | Final Inspection - Building Department | 2 | 2 | 21-May-15 | 22-May-15 | 0 |
| CM-1022 | Podium - "Clean/Punch" Complete - All Floors, All Zon | 0 | 0 | | 22-May-15 | 0 |
| L03-8680 | Final Cleaning at Pool | 2 | 2 | 28-May-15 | 29-May-15 | 4 |
| L03-8678 | Owner Punchlist at Pool (inspect/distribute/correct) | 3 | 3 | 01-Jun-15 | 03-Jun-15 | 4 |
| CO-7168 | Final Inspections - Pool | 5 | 5 | 04-Jun-15 | 10-Jun-15 | 4 |
| SW-2228 | Zone 2 - Pull wire and install light poles | 5 | 5 | 09-Jun-15 | 15-Jun-15 | 0 |
| SW-2232 | Zone 2 - Replace luminaire north of 3rd | 1 | 1 | 09-Jun-15 | 09-Jun-15 | 4 |
| SW-2328 | Zone 3 - Pull wire and install light poles | 5 | 5 | 09-Jun-15 | 15-Jun-15 | 0 |
| SW-2056 | Zone 4 - Pull wire and replace luminaires on 110th | 5 | 5 | 09-Jun-15 | 15-Jun-15 | 0 |
| CO-7170 | Final inspections - Site Lighting | 1 | 1 | 16-Jun-15 | 16-Jun-15 | 0 |
| CO-7008 | Substantial Completion - Pool & Site Lighting | 0 | 0 | | 16-Jun-15 | 0 |
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13 A | | |
| CM-1002 | CM - Contract Time (578 Cal Days) | 576 | 0 | 06-Mar-13 A | 05-Oct-14 A | |
| CM-1014 | CM - Start of Construction | 0 | 0 | 05-Apr-13 A | | |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 09-Mar-15 A | | |
| CM-1016 | CM - Owner FF+E "Build-Out" - Floors 4 & 5 | 7 | 0 | 09-Mar-15 A | 15-Mar-15 A | |
| CM-1006 | Construction Documents Issued by Client - (Due on 7 | 0 | 0 | 13-Apr-15 | | 40 |
| CM-1008 | Finalization of Allowances - (Due on 9-2-13) | 0 | 0 | 13-Apr-15 | | 40 |
| CM-1018 | CM - Hotel Operations Training | 14 | 14 | 30-Apr-15 | 13-May-15 | 9 |
| CO-7004 | CO - Prep / Submit O&M Manuals | 14 | 14 | 30-Apr-15 | 13-May-15 | 9 |
| CO-7006 | CO - Certificate of Occupancy/Substantial Completior | 0 | 0 | | 22-May-15* | 0 |
| CO-7122 | CO - Certificate of Occupancy | 0 | 0 | | 22-May-15 | 0 |

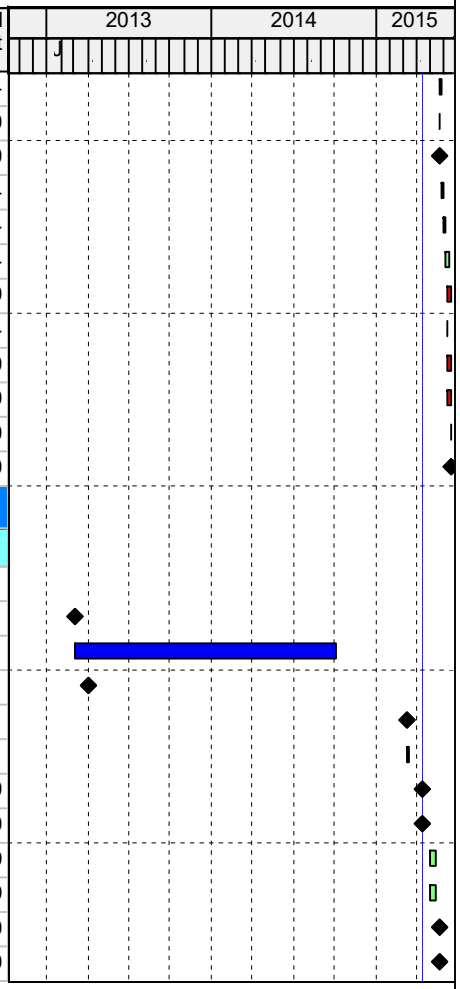



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Misc Milestones** | | | | | | |
| CM-1020 | MM - Site Mobilization | 10 | 0 | 06-Mar-13 A | 04-Apr-13 A | |
| MM-1008 | MM - Top Out - Tower / Structure | 0 | 0 | | 16-Apr-14 A | |
| MM-1004 | MM - Start Drywall In Tower | 0 | 0 | 27-Jun-14 A | | |
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 06-Sep-14 A | |
| MM-1010 | Energize Permanent Power | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| *Tower Crane* | | | | | | |
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 0 | 04-Jun-13 A | 14-Jun-13 A | |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 0 | 20-Jun-13 A | 24-Jun-13 A | |
| TC-5902 | Tower Crane - Erectiion | 2 | 0 | 21-Jun-13 A | 24-Jun-13 A | |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 24-Jun-13 A | | |
| TC-5906 | Tower Crane - Operatational Period | 391 | 0 | 24-Jun-13 A | 16-Jun-14 A | |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 0 | 16-Jun-14 A | 17-Jun-14 A | |
| *Man & Material Lifts* | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 0 | 14-Jan-14 A | 20-Jan-14 A | |
| ML-5952 | Man/Material Lifts - Erect/Build Loading Dock | 5 | 0 | 21-Jan-14 A | 27-Jan-14 A | |
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 10-Feb-14 A | | |
| ML-5954 | Man/Material Lifts - Load Test / Certify | 1 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| ML-5958 | Man/Material Lifts - Operatational Period | 196 | 0 | 10-Feb-14 A | 15-Nov-14 A | |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 2 | 0 | 15-Nov-14 A | 16-Nov-14 A | |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |
| *Mass Excavation / Shoring* | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 0 | 05-Apr-13 A | 12-Apr-13 A | |
| SW-2002 | Demolition And Utility Relocation | 8 | 0 | 15-Apr-13 A | 19-Apr-13 A | |

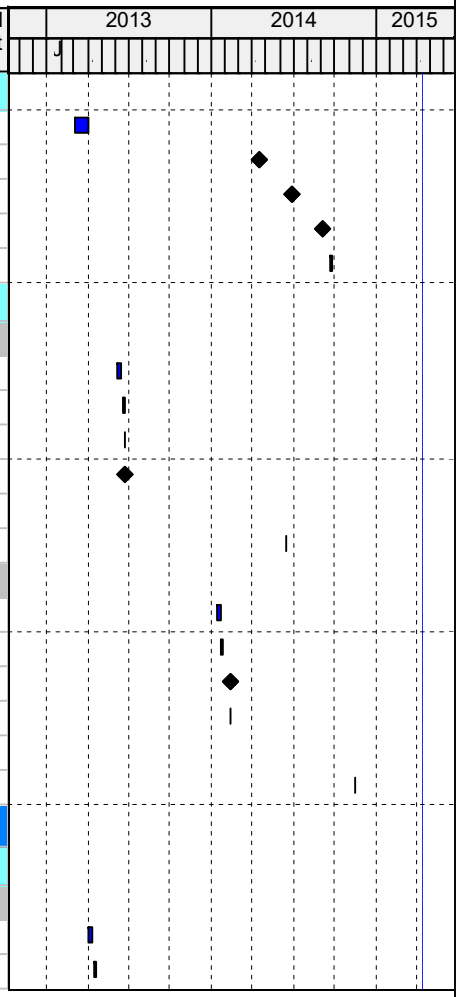



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2010 | Grade Subgrade for Elect/Plumbing | 3 | 0 | 07-Jan-14 A | 09-Jan-14 A | |
| **Site Finishes** | | | | | | |
| SW-2006 | Install Perm Power Electrical Service / Dry Utilities (Ofl | 15 | 0 | 20-May-14 A | 05-Jun-14 A | |
| SW-2004 | Offsite Water & Water Connection | 9 | 0 | 22-Sep-14 A | 01-Oct-14 A | |
| SW-2008 | Zone 4 - Landscaping & irrigation | 15 | 15 | 13-Apr-15 | 01-May-15 | 8 |
| **Structure** | | | | | | |
| **Foundation / Substructure - (Levels LL4 / LL3)** | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 0 | 12-Jun-13 A | 27-Jun-13 A | |
| LL4-1601 | LL4 - Excavate Footings | 14 | 0 | 17-Jun-13 A | 30-Jul-13 A | |
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 0 | 18-Jun-13 A | 24-Jun-13 A | |
| LL4-1606 | LL4 - Undrgmd Plumbing | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-1608 | LL4 - Undrgmd Elec | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 0 | 19-Jun-13 A | 25-Jun-13 A | |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 0 | 26-Jun-13 A | 02-Aug-13 A | |
| LL4-2033 | LL4 - Shotcrete Walls | 27 | 0 | 26-Jun-13 A | 05-Aug-13 A | |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 0 | 03-Jul-13 A | 21-Aug-13 A | |
| LL4-1614 | LL4 - FRP SOG | 5 | 0 | 10-Jul-13 A | 07-Aug-13 A | |
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 0 | 12-Jul-13 A | 26-Jul-13 A | |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 0 | 13-Jul-13 A | 06-Aug-13 A | |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 0 | 22-Jul-13 A | 24-Jul-13 A | |
| LL4-1618 | LL4 - FRP Ramp SOG | 5 | 0 | 01-Aug-13 A | 07-Aug-13 A | |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2004 | LL2 - Shore / Form Deck | 8 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2006 | LL3 - M & E Inserts | 4 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2008 | LL3 - ReSteel / PT Cables | 6 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2010 | LL3 - Install Embeds | 2 | 0 | 05-Aug-13 A | 09-Aug-13 A | |

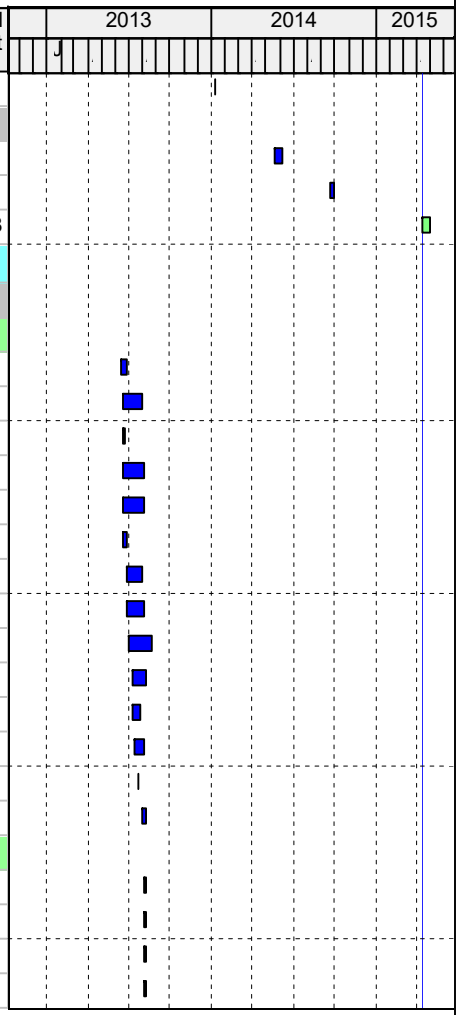



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-2001 | LL3 - Waterproof Walls | 3 | 0 | 05-Aug-13 A | 05-Aug-13 A | |
| LL3-2012 | LL3 - Pour / Finish Deck | 2 | 0 | 16-Aug-13 A | 16-Aug-13 A | |
| LL3-2014 | LL3 - Stress Tendons | 1 | 0 | 19-Aug-13 A | 19-Aug-13 A | |
| LL3-2000 | LL3 - FRP Core Walls | 8 | 0 | 19-Aug-13 A | 28-Aug-13 A | |
| LL3-2033 | LL3 - Shotcrete Walls | 5 | 0 | 23-Aug-13 A | 26-Aug-13 A | |
| LL3-2016 | LL3 - Strip / ReShore Deck | 3 | 0 | 01-Sep-13 A | 13-Sep-13 A | |
| LL3-2018 | LL3 - Remove ReShores | 4 | 0 | 04-Nov-13 A | 07-Nov-13 A | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Grids 1 to 4 - (SOG @ Loading Dock)** | | | | | | |
| LL2-2056 | LL2 - Grease Intercepter | 5 | 0 | 15-Aug-13 A | 21-Aug-13 A | |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 0 | 27-Aug-13 A | 04-Sep-13 A | |
| LL2-2027 | LL2 - Waterproof Walls | 2 | 0 | 27-Aug-13 A | 28-Aug-13 A | |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 0 | 30-Aug-13 A | 05-Sep-13 A | |
| LL2-2021 | LL2 - FRP Elec Vault | 14 | 0 | 30-Aug-13 A | 04-Sep-13 A | |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 0 | 04-Sep-13 A | 11-Sep-13 A | |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 0 | 11-Sep-13 A | 13-Sep-13 A | |
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls/Roof | 11 | 0 | 19-Sep-13 A | 03-Oct-13 A | |
| LL2-2020 | LL2 - Undrgmd Plumbing | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2022 | LL2 - Undrgmd Elec | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2031 | LL2 - FRP Generator SOG | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2015 | LL2 to LL1 FRP Columns / Misc Walls | 6 | 0 | 01-Oct-13 A | 01-Oct-13 A | |
| LL2-2029 | LL2 - F/R/P Pour #2 | 8 | 0 | 15-Jan-14 A | 24-Jan-14 A | |
| LL2-2011 | LL2 - F/R/P Pour #3 | 16 | 0 | 24-Jan-14 A | 18-Feb-14 A | |
| LL2-2019 | LL2 - F/R/P Pour #6 | 4 | 0 | 19-Feb-14 A | 17-Mar-14 A | |
| LL2-2044 | LL2 - Set Generator | 1 | 0 | 16-May-14 A | 16-May-14 A | |

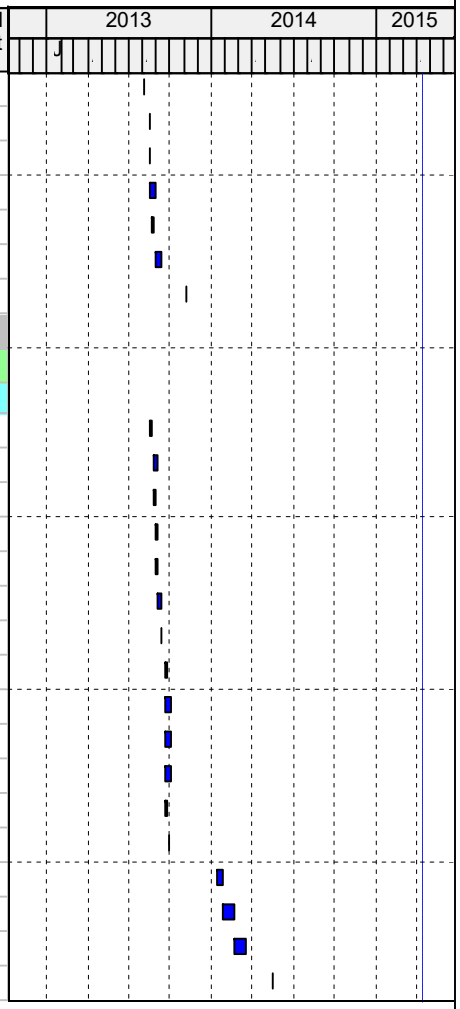


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |
| LL2-2004 | LL2 - Shore / Form Deck | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2035 | LL2 to LL1 - Shotcrete Walls | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2006 | LL2 - M & E Inserts | 4 | 0 | 14-Aug-13 A | 19-Aug-13 A | |
| LL2-2008 | LL2 - ReSteel / PT Cables | 6 | 0 | 14-Aug-13 A | 21-Aug-13 A | |
| LL2-2010 | LL2 - Install Embeds | 3 | 0 | 14-Aug-13 A | 16-Aug-13 A | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 0 | 27-Aug-13 A | 06-Sep-13 A | |
| LL2-2012 | LL2 - Place / Finish Deck | 3 | 0 | 29-Aug-13 A | 29-Aug-13 A | |
| LL2-2023 | LL2 - Waterproof Walls | 3 | 0 | 29-Aug-13 A | 03-Sep-13 A | |
| LL2-2014 | LL2 - Stress Tendons | 1 | 0 | 30-Aug-13 A | 30-Aug-13 A | |
| LL2-2016 | LL2 - Strip / ReShore | 3 | 0 | 03-Sep-13 A | 05-Sep-13 A | |
| LL2-8234 | LL2 - Place / Finish Deck | 3 | 0 | 12-Sep-13 A | 12-Sep-13 A | |
| LL2-2000 | LL2 - FRP Core Walls | 8 | 0 | 12-Sep-13 A | 23-Sep-13 A | |
| LL2-2018 | LL2 - Remove ReShores | 4 | 0 | 13-Nov-13 A | 18-Nov-13 A | |
| LL2-2013 | LL2 - F/R/P Pour #1 | 4 | 0 | 13-Jan-14 A | 16-Jan-14 A | |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| P5A-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2000 | LL1 - FRP Core Walls | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2004 | LL1 - Shore / Form Deck | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| P6-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P6-2004 | LL1 - Shore / Form Deck | 7 | 0 | 16-Sep-13 A | 24-Sep-13 A | |
| P5A-2006 | LL1 - MEP Rough In | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2008 | LL1 - ReSteel / PT Cables | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2012 | LL1 - Place / Finish Deck | 0 | 0 | 20-Sep-13 A | | |
| P5A-2020 | LL1 - Waterproof Walls | 3 | 0 | 20-Sep-13 A | 24-Sep-13 A | |
| P5A-2014 | LL1 - Stress Tendons | 1 | 0 | 23-Sep-13 A | 23-Sep-13 A | |

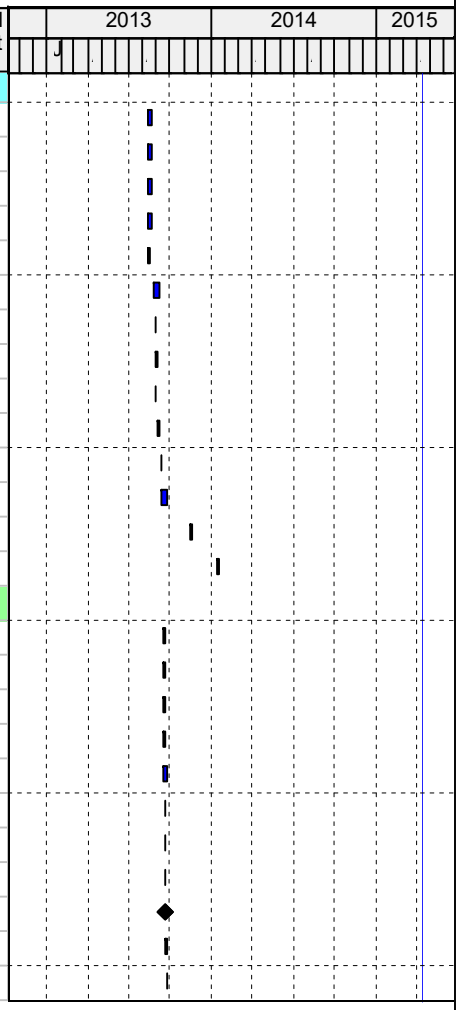



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P5A-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2006 | LL1 - MEP Rough In | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2008 | LL1 - ReSteel / PT Cables | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 24-Sep-13 A | 25-Sep-13 A | |
| P6-2020 | LL1 - Waterproof Walls | 4 | 0 | 24-Sep-13 A | 27-Sep-13 A | |
| P5A-2033 | LL1 - Resteel/Shotcrete Walls | 3 | 0 | 25-Sep-13 A | 27-Sep-13 A | |
| P5B-2002 | LL1 - FRP Columns Below | 5 | 0 | 26-Sep-13 A | 02-Oct-13 A | |
| P5B-2004 | LL1 - Shore / Form Deck | 7 | 0 | 26-Sep-13 A | 04-Oct-13 A | |
| P6-2012 | LL1 - Place / Finish Deck | 0 | 0 | 27-Sep-13 A | | |
| P6-2014 | LL1 - Stress Tendons | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2033 | LL1 - Resteel/Shotcrete Walls | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 01-Oct-13 A | 03-Oct-13 A | |
| P5B-2006 | LL1 - MEP Rough In | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2002 | FRP Columns Below | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2004 | Shore / Form Deck | 4 | 0 | 03-Oct-13 A | 08-Oct-13 A | |
| P5B-2008 | LL1 - ReSteel / PT Cables | 5 | 0 | 04-Oct-13 A | 10-Oct-13 A | |
| P5B-2010 | LL1 - Install Edgeform/Embeds | 4 | 0 | 04-Oct-13 A | 09-Oct-13 A | |
| P8-2002 | FRP Columns Below | 5 | 0 | 07-Oct-13 A | 11-Oct-13 A | |
| P8-2000 | Form/Resteel/Close Core Walls | 14 | 0 | 07-Oct-13 A | 24-Oct-13 A | |
| P8-2004 | Shore / Form Deck P8 | 8 | 0 | 07-Oct-13 A | 16-Oct-13 A | |
| P7-2002 | FRP Columns Below | 5 | 0 | 08-Oct-13 A | 14-Oct-13 A | |
| P7-2004 | Shore / Form Deck | 6 | 0 | 08-Oct-13 A | 15-Oct-13 A | |
| P10A--2006 | MEP Rough In | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2008 | ReSteel / PT Cables | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2010 | Install Edgeform/Embeds | 2 | 0 | 08-Oct-13 A | 09-Oct-13 A | |
| P5B-2012 | LL1 - Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P10A--2012 | Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |

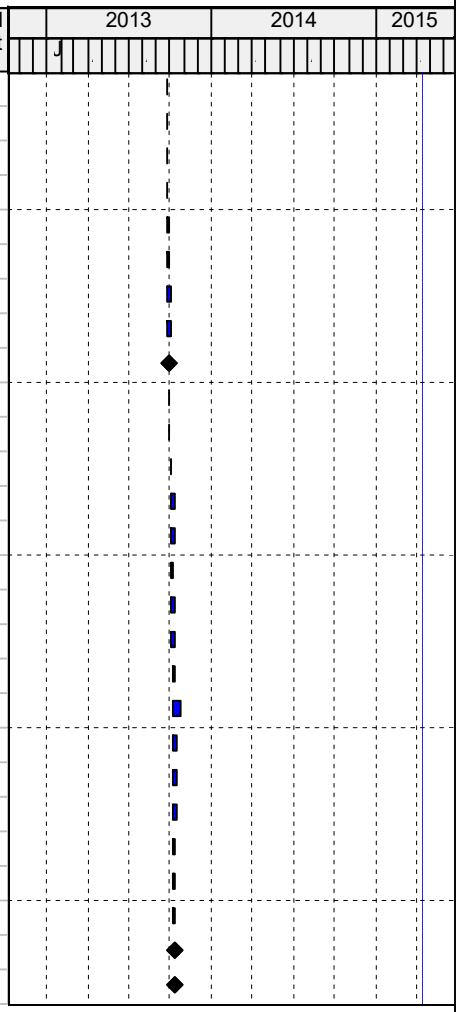



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P5B-2014 | LL1 - Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P7-2006 | MEP Rough In | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P7-2008 | ReSteel / PT Cables | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P10A--2014 | Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P8-2020 | Shore / Form Deck P9 | 6 | 0 | 14-Oct-13 A | 21-Oct-13 A | |
| P5B-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2010 | Install Edgeform/Embeds | 2 | 0 | 15-Oct-13 A | 16-Oct-13 A | |
| P8-2006 | MEP Rough In | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2008 | ReSteel / PT Cables | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2010 | Install Edgeform/Embeds | 4 | 0 | 15-Oct-13 A | 18-Oct-13 A | |
| P10A--2016 | Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2012 | Place / Finish Deck | 0 | 0 | 18-Oct-13 A | | |
| P7-2033 | Resteel/Shotcrete Walls | 3 | 0 | 18-Oct-13 A | 22-Oct-13 A | |
| P7-2014 | Stress Tendons | 1 | 0 | 21-Oct-13 A | 21-Oct-13 A | |
| P7-2016 | Strip / ReShore Deck | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2002 | FRP Columns Below | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P10B--2000 | FRP Shear Walls Below | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2004 | Shore / Form Deck | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P8-2012 | Place / Finish Deck P 8 & 9 and Core Walls | 0 | 0 | 25-Oct-13 A | | |
| P8-2014 | Stress Tendons | 1 | 0 | 28-Oct-13 A | 28-Oct-13 A | |
| P10B--2006 | MEP Rough In | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2008 | ReSteel / PT Cables | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2010 | Install Edgeform/Embeds | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P12--2002 | FRP Columns Below | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P12--2000 | Form/Resteel/Close Core Walls | 9 | 0 | 28-Oct-13 A | 07-Nov-13 A | |
| P12--2004 | Shore / Form Deck | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P8-2016 | Strip / ReShore Deck | 3 | 0 | 29-Oct-13 A | 31-Oct-13 A | |

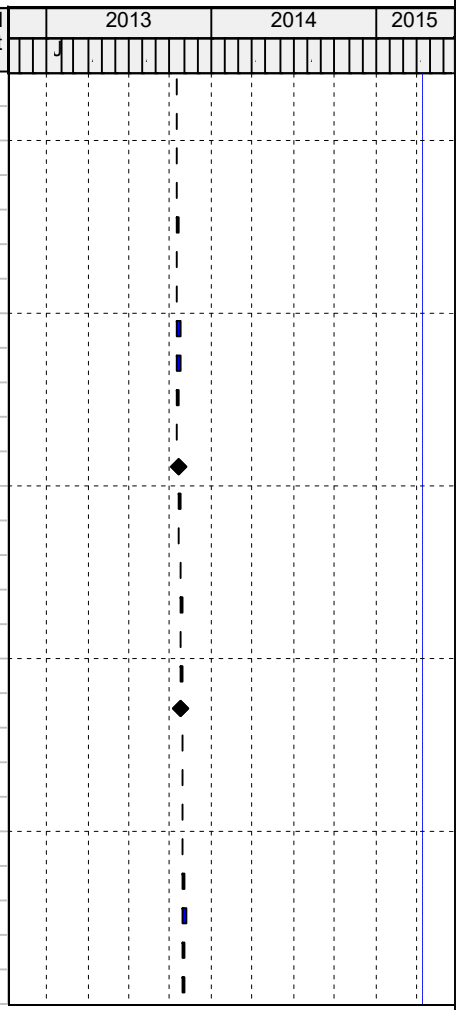



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P11–2002 | FRP Columns Below | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P11–2004 | Shore / Form Deck | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P10B–2012 | Place / Finish Deck | 0 | 0 | 31-Oct-13 A | | |
| P10B–2014 | Stress Tendons | 1 | 0 | 01-Nov-13 A | 01-Nov-13 A | |
| P12–2006 | MEP Rough In | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12–2008 | ReSteel / PT Cables | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12–2010 | Install Edgeform/Embeds | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P10B–2016 | Strip / ReShore Deck | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2006 | MEP Rough In | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2008 | ReSteel / PT Cables | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2010 | Install Edgeform/Embeds | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2012 | Place / Finish Deck | 0 | 0 | 07-Nov-13 A | | |
| P13–2002 | FRP Columns Below | 5 | 0 | 07-Nov-13 A | 14-Nov-13 A | |
| P13–2004 | Shore / Form Deck | 9 | 0 | 07-Nov-13 A | 28-Nov-13 A | |
| P11–2014 | Stress Tendons | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| P12–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 08-Nov-13 A | | |
| P11–2016 | Strip / ReShore Deck | 3 | 0 | 12-Nov-13 A | 14-Nov-13 A | |
| P12–2014 | Stress Tendons | 1 | 0 | 12-Nov-13 A | 12-Nov-13 A | |
| P14–2002 | FRP Columns Below | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P14–2000 | Form/Resteel/Close Core Walls | 8 | 0 | 19-Nov-13 A | 03-Dec-13 A | |
| P14–2004 | Shore / Form Deck | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P13A–2002 | FRP Columns Below | 5 | 0 | 21-Nov-13 A | 27-Nov-13 A | |
| P13A–2004 | Shore / Form Deck | 4 | 0 | 21-Nov-13 A | 26-Nov-13 A | |
| P13–2010 | Install Edgeform/Embeds | 5 | 0 | 22-Nov-13 A | 04-Dec-13 A | |
| P13–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2006 | MEP Rough In | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |

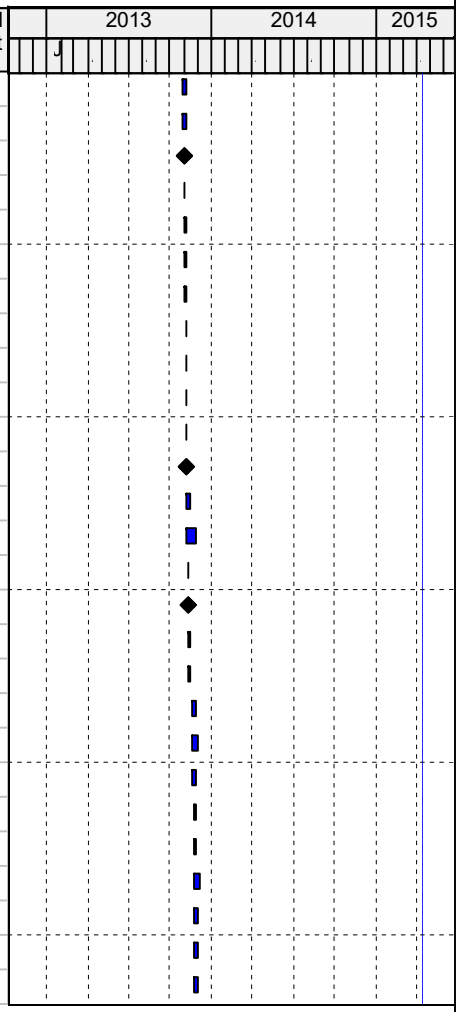



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P14–2010 | Install Edgeform/Embeds | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P13–2006 | MEP Rough In | 5 | 0 | 26-Nov-13 A | 03-Dec-13 A | |
| P13A–2006 | MEP Rough In | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2008 | ReSteel / PT Cables | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2010 | Install Edgeform/Embeds | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13–2012 | Place / Finish Deck | 0 | 0 | 02-Dec-13 A | | |
| P13A–2012 | Place / Finish Deck | 0 | 0 | 03-Dec-13 A | | |
| P14–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 04-Dec-13 A | | |
| P13–2014 | Stress Tendons | 1 | 0 | 05-Dec-13 A | 05-Dec-13 A | |
| P15–2002 | FRP Columns Below | 3 | 0 | 05-Dec-13 A | 09-Dec-13 A | |
| P15–2000 | Jump/Resteel/Close Core | 9 | 0 | 05-Dec-13 A | 17-Dec-13 A | |
| P15–2004 | Shore / Form Deck | 5 | 0 | 05-Dec-13 A | 11-Dec-13 A | |
| P13–2016 | Strip / ReShore Deck | 3 | 0 | 06-Dec-13 A | 10-Dec-13 A | |
| P13A–2014 | Stress Tendons | 1 | 0 | 06-Dec-13 A | 06-Dec-13 A | |
| P14–2014 | Stress Tendons | 1 | 0 | 07-Dec-13 A | 07-Dec-13 A | |
| P15–2006 | MEP Rough In | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2008 | ReSteel / PT Cables | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2010 | Install Edgeform/Embeds | 3 | 0 | 11-Dec-13 A | 13-Dec-13 A | |
| P16-2002 | FRP Columns Below | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P16-2004 | Shore / Form Deck | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P15–2012 | Place / Finish Deck | 0 | 0 | 18-Dec-13 A | | |
| P15–2020 | Place Conc @ Core | 0 | 0 | 18-Dec-13 A | | |
| P16-2000 | Jump/Resteel/Close Core | 5 | 0 | 18-Dec-13 A | 24-Dec-13 A | |
| P16-2006 | MEP Rough In | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2008 | ReSteel / PT Cables | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2010 | Install Edgeform/Embeds | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P15–2014 | Stress Tendons | 1 | 0 | 21-Dec-13 A | 21-Dec-13 A | |

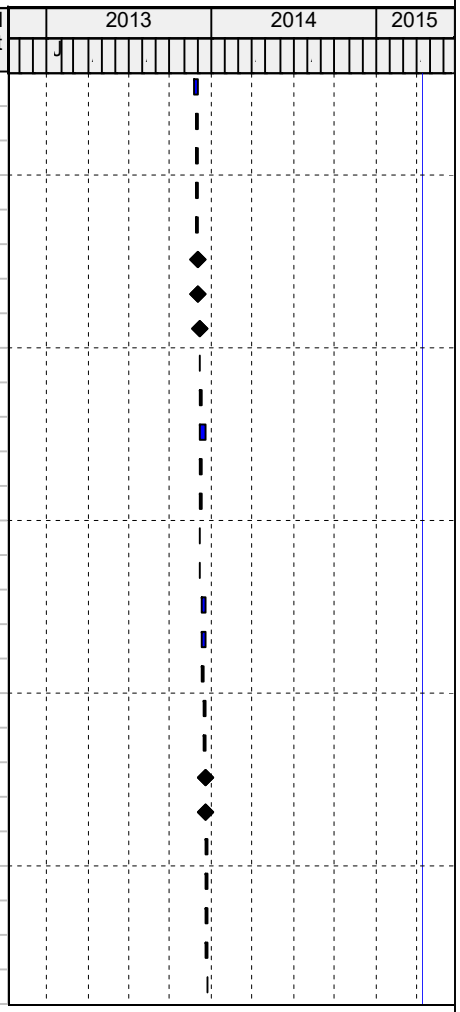



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P8-2018 | Remove Reshores | 2 | 0 | 23-Dec-13 A | 24-Dec-13 A | |
| P10A--2018 | Remove Reshores | 2 | 0 | 26-Dec-13 A | 27-Dec-13 A | |
| P16-2012 | Place / Finish Deck | 0 | 0 | 26-Dec-13 A | | |
| P16-2020 | Place Conc @ Core | 0 | 0 | 26-Dec-13 A | | |
| P17-2002 | FRP Columns Below | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P17-2000 | Jump/Resteel/Close Core | 7 | 0 | 27-Dec-13 A | 07-Jan-14 A | |
| P17-2004 | Shore / Form Deck | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P10B--2018 | Remove Reshores | 2 | 0 | 30-Dec-13 A | 31-Dec-13 A | |
| P16-2014 | Stress Tendons | 1 | 0 | 31-Dec-13 A | 31-Dec-13 A | |
| P5A-2018 | LL1 - Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P11--2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P12--2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P17-2006 | MEP Rough In | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2008 | ReSteel / PT Cables | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2010 | Install Edgeform/Embeds | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P6-2018 | LL1 - Remove Reshores | 2 | 0 | 06-Jan-14 A | 07-Jan-14 A | |
| P5B-2018 | LL1 - Remove Reshores | 2 | 0 | 08-Jan-14 A | 09-Jan-14 A | |
| P17-2012 | Place / Finish Deck | 0 | 0 | 08-Jan-14 A | | |
| P17-2020 | Place Conc @ Core | 0 | 0 | 08-Jan-14 A | | |
| P18-2002 | FRP Columns Below | 5 | 0 | 09-Jan-14 A | 15-Jan-14 A | |
| P18-2000 | Jump/Resteel/Close Core | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P18-2004 | Shore / Form Deck | 3 | 0 | 09-Jan-14 A | 13-Jan-14 A | |
| LL2-2022R | MEP Rough In | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P7-2018 | Remove Reshores | 2 | 0 | 10-Jan-14 A | 13-Jan-14 A | |
| P17-2014 | Stress Tendons | 1 | 0 | 11-Jan-14 A | 11-Jan-14 A | |
| P13--2018 | Remove Reshores | 2 | 0 | 13-Jan-14 A | 14-Jan-14 A | |
| P13A--2018 | Remove Reshores | 2 | 0 | 15-Jan-14 A | 16-Jan-14 A | |

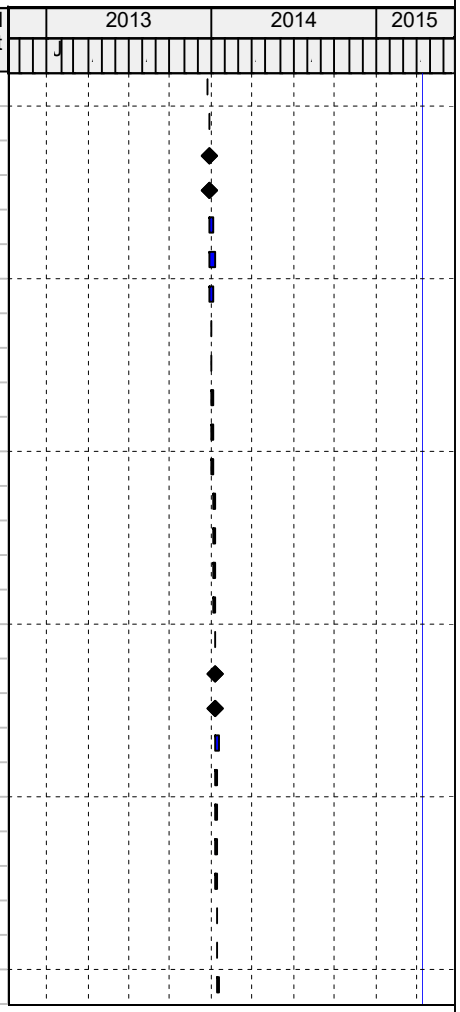


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| WEA-2012 | WIND IMPACT | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| P18-2006 | MEP Rough In | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2008 | ReSteel / PT Cables | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2010 | Install Edgeform/Embeds | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2012 | Place / Finish Deck | 0 | 0 | 22-Jan-14 A | | |
| P18-2020 | Place Conc @ Core | 0 | 0 | 22-Jan-14 A | | |
| P19-2002 | FRP Columns Below | 5 | 0 | 23-Jan-14 A | 29-Jan-14 A | |
| P19-2000 | Jump/Resteel/Close Core | 4 | 0 | 23-Jan-14 A | 28-Jan-14 A | |
| P19-2004 | Shore / Form Deck | 3 | 0 | 23-Jan-14 A | 27-Jan-14 A | |
| P18-2014 | Stress Tendons | 1 | 0 | 25-Jan-14 A | 25-Jan-14 A | |
| P14–2018 | Remove Reshores | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2006 | MEP Rough In | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2008 | ReSteel / PT Cables | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2010 | Install Edgeform/Embeds | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2012 | Place / Finish Deck | 0 | 0 | 29-Jan-14 A | | |
| P19-2020 | Place Conc @ Core | 0 | 0 | 29-Jan-14 A | | |
| P20-2002 | FRP Columns Below | 5 | 0 | 30-Jan-14 A | 05-Feb-14 A | |
| P20-2000 | Jump/Resteel/Close Core | 9 | 0 | 30-Jan-14 A | 11-Feb-14 A | |
| P20-2004 | Shore / Form Deck | 6 | 0 | 30-Jan-14 A | 10-Feb-14 A | |
| P19-2014 | Stress Tendons | 1 | 0 | 01-Feb-14 A | 01-Feb-14 A | |
| P13A–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P14–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P15–2016 | Strip / ReShore Deck | 3 | 0 | 06-Feb-14 A | 10-Feb-14 A | |
| P20-2006 | MEP Rough In | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2008 | ReSteel / PT Cables | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2010 | Install Edgeform/Embeds | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| L03-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 06-Feb-14 A | 12-Feb-14 A | |

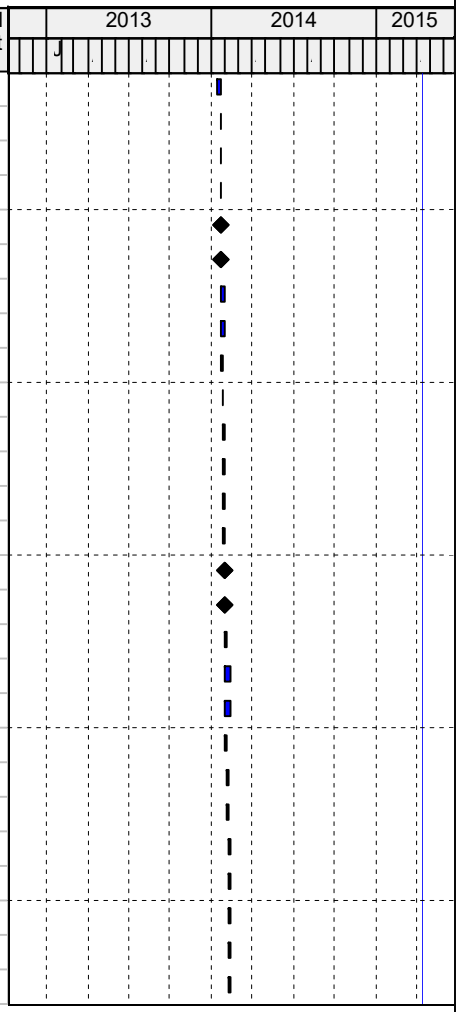


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P16-2016 | Strip / ReShore Deck | 3 | 0 | 10-Feb-14 A | 12-Feb-14 A | |
| L04-2018 | Remove Reshores | 2 | 0 | 10-Feb-14 A | 11-Feb-14 A | |
| L03-2018 | Remove Reshores | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| P17-2016 | Strip / ReShore Deck | 3 | 0 | 12-Feb-14 A | 14-Feb-14 A | |
| P20-2012 | Place / Finish Deck | 0 | 0 | 12-Feb-14 A | | |
| P20-2020 | Place Conc @ Core | 0 | 0 | 12-Feb-14 A | | |
| L04-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-Feb-14 A | 18-Feb-14 A | |
| P12–2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P18-2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P21-2002 | FRP Columns Below | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| P21-2000 | Jump/Resteel/Close Core | 4 | 0 | 13-Feb-14 A | 18-Feb-14 A | |
| P21-2004 | Shore / Form Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P19-2016 | Strip / ReShore Deck | 3 | 0 | 14-Feb-14 A | 18-Feb-14 A | |
| P20-2014 | Stress Tendons | 1 | 0 | 15-Feb-14 A | 15-Feb-14 A | |
| P21-2006 | MEP Rough In | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2008 | ReSteel / PT Cables | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P20-2016 | Strip / ReShore Deck | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| L05-2018 | Remove Reshores | 2 | 0 | 18-Feb-14 A | 19-Feb-14 A | |
| P21-2012 | Place / Finish Deck | 0 | 0 | 19-Feb-14 A | | |
| P21-2020 | Place Conc @ Core | 0 | 0 | 19-Feb-14 A | | |
| P22-2002 | FRP Columns Below | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P22-2000 | Jump/Resteel/Close Core | 4 | 0 | 20-Feb-14 A | 25-Feb-14 A | |
| P22-2004 | Shore / Form Deck | 3 | 0 | 20-Feb-14 A | 24-Feb-14 A | |
| L05-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P21-2014 | Stress Tendons | 1 | 0 | 22-Feb-14 A | 22-Feb-14 A | |
| P21-2016 | Strip / ReShore Deck | 3 | 0 | 24-Feb-14 A | 26-Feb-14 A | |

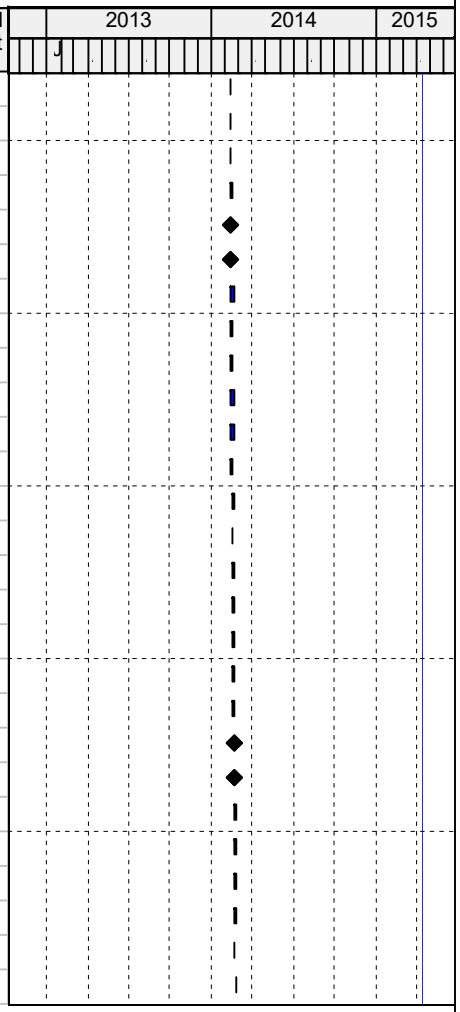



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P22-2006 | MEP Rough In | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2008 | ReSteel / PT Cables | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| L06-2018 | Remove Reshores | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| P22-2012 | Place / Finish Deck | 0 | 0 | 26-Feb-14 A | | |
| P22-2020 | Place Conc @ Core | 0 | 0 | 26-Feb-14 A | | |
| P23-2002 | FRP Columns Below | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2000 | Jump/Resteel/Close Core | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2004 | Shore / Form Deck | 3 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2006 | MEP Rough In | 2 | 0 | 01-Mar-14 A | 03-Mar-14 A | |
| P22-2014 | Stress Tendons | 1 | 0 | 01-Mar-14 A | 01-Mar-14 A | |
| P23-2008 | ReSteel / PT Cables | 2 | 0 | 03-Mar-14 A | 04-Mar-14 A | |
| P22-2016 | Strip / ReShore Deck | 3 | 0 | 04-Mar-14 A | 10-Mar-14 A | |
| P23-2010 | Install Edgeform/Embeds | 2 | 0 | 04-Mar-14 A | 04-Mar-14 A | |
| L07-2018 | Remove Reshores | 2 | 0 | 04-Mar-14 A | 05-Mar-14 A | |
| P23-2012 | Place / Finish Deck | 0 | 0 | 05-Mar-14 A | | |
| P23-2020 | Place Conc @ Core | 0 | 0 | 05-Mar-14 A | | |
| P24-2002 | FRP Columns Below | 5 | 0 | 05-Mar-14 A | 07-Mar-14 A | |
| P24-2004 | Shore / Form Deck | 3 | 0 | 06-Mar-14 A | 10-Mar-14 A | |
| P24-2000 | Jump/Resteel/Close Core | 4 | 0 | 08-Mar-14 A | 10-Mar-14 A | |
| P23-2014 | Stress Tendons | 1 | 0 | 10-Mar-14 A | 10-Mar-14 A | |
| P24-2008 | ReSteel / PT Cables | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P24-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P23-2016 | Strip / ReShore Deck | 3 | 0 | 11-Mar-14 A | 17-Mar-14 A | |
| P24-2006 | MEP Rough In | 2 | 0 | 11-Mar-14 A | 11-Mar-14 A | |
| P25-2002 | FRP Columns Below | 5 | 0 | 11-Mar-14 A | 13-Mar-14 A | |
| L08-2018 | Remove Reshores | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |

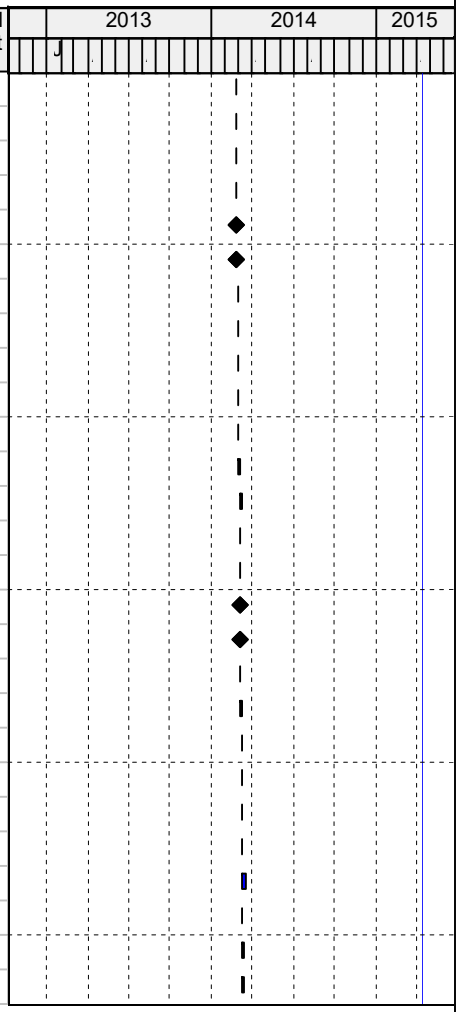



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P24-2012 | Place / Finish Deck | 0 | 0 | 12-Mar-14 A | | |
| P24-2020 | Place Conc @ Core | 0 | 0 | 12-Mar-14 A | | |
| P25-2004 | Shore / Form Deck | 3 | 0 | 13-Mar-14 A | 17-Mar-14 A | |
| P25-2000 | Jump/Resteel/Close Core | 4 | 0 | 15-Mar-14 A | 17-Mar-14 A | |
| P24-2014 | Stress Tendons | 1 | 0 | 17-Mar-14 A | 17-Mar-14 A | |
| P25-2006 | MEP Rough In | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2008 | ReSteel / PT Cables | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| L06-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 18-Mar-14 A | 20-Mar-14 A | |
| L09-2018 | Remove Reshores | 2 | 0 | 18-Mar-14 A | 19-Mar-14 A | |
| P26-2002 | FRP Columns Below | 5 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| P25-2012 | Place / Finish Deck | 0 | 0 | 19-Mar-14 A | | |
| P25-2020 | Place Conc @ Core | 0 | 0 | 19-Mar-14 A | | |
| P26-2004 | Shore / Form Deck | 3 | 0 | 20-Mar-14 A | 24-Mar-14 A | |
| L07-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 21-Mar-14 A | 25-Mar-14 A | |
| P26-2000 | Jump/Resteel/Close Core | 4 | 0 | 22-Mar-14 A | 24-Mar-14 A | |
| P26-2006 | MEP Rough In | 2 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P26-2008 | ReSteel / PT Cables | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P26-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P25-2014 | Stress Tendons | 1 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P27-2002 | FRP Columns Below | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| P26-2012 | Place / Finish Deck | 0 | 0 | 26-Mar-14 A | | |
| P26-2020 | Place Conc @ Core | 0 | 0 | 26-Mar-14 A | | |
| L08-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 26-Mar-14 A | 28-Mar-14 A | |
| L10-2018 | Remove Reshores | 2 | 0 | 26-Mar-14 A | 27-Mar-14 A | |
| P27-2004 | Shore / Form Deck | 3 | 0 | 27-Mar-14 A | 31-Mar-14 A | |
| P27-2000 | Jump/Resteel/Close Core | 4 | 0 | 29-Mar-14 A | 31-Mar-14 A | |

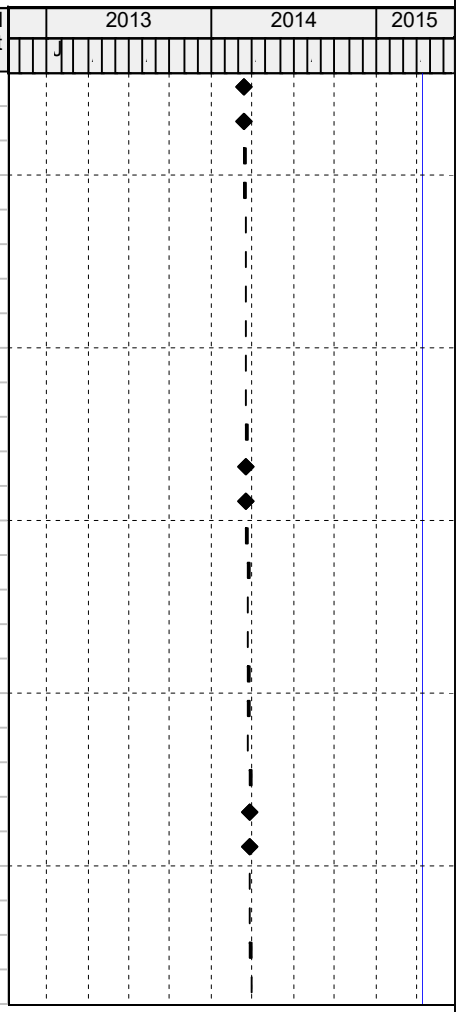



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P27-2006 | MEP Rough In | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2008 | ReSteel / PT Cables | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2010 | Install Edgeform/Embeds | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P26-2014 | Stress Tendons | 1 | 0 | 31-Mar-14 A | 31-Mar-14 A | |
| L09-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 31-Mar-14 A | 02-Apr-14 A | |
| P24-2016 | Strip / ReShore Deck | 3 | 0 | 01-Apr-14 A | 07-Apr-14 A | |
| L11-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 02-Apr-14 A | |
| L12-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 03-Apr-14 A | |
| P27-2012 | Place / Finish Deck | 0 | 0 | 02-Apr-14 A | | |
| P27-2020 | Place Conc @ Core | 0 | 0 | 02-Apr-14 A | | |
| P28-2002 | FRP Columns Below | 5 | 0 | 02-Apr-14 A | 04-Apr-14 A | |
| P28-2004 | Shore / Form Deck | 4 | 0 | 03-Apr-14 A | 08-Apr-14 A | |
| L10-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| P27-2014 | Stress Tendons | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| P25-2016 | Strip / ReShore Deck | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L14-2018 | Remove Reshores | 2 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| P28-2000 | Jump/Resteel/Close Core | 7 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| P28-2006 | MEP Rough In | 4 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2008 | ReSteel / PT Cables | 4 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Apr-14 A | 11-Apr-14 A | |
| L12-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| P28-2012 | Place / Finish Deck | 0 | 0 | 14-Apr-14 A | | |
| P28-2020 | Place Conc @ Core | 0 | 0 | 14-Apr-14 A | | |
| P29-2002 | FRP Columns Above Roof Deck | 3 | 0 | 14-Apr-14 A | 18-Apr-14 A | |
| P26-2016 | Strip / ReShore Deck | 3 | 0 | 14-Apr-14 A | 17-Apr-14 A | |
| L14-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-Apr-14 A | 18-Apr-14 A | |

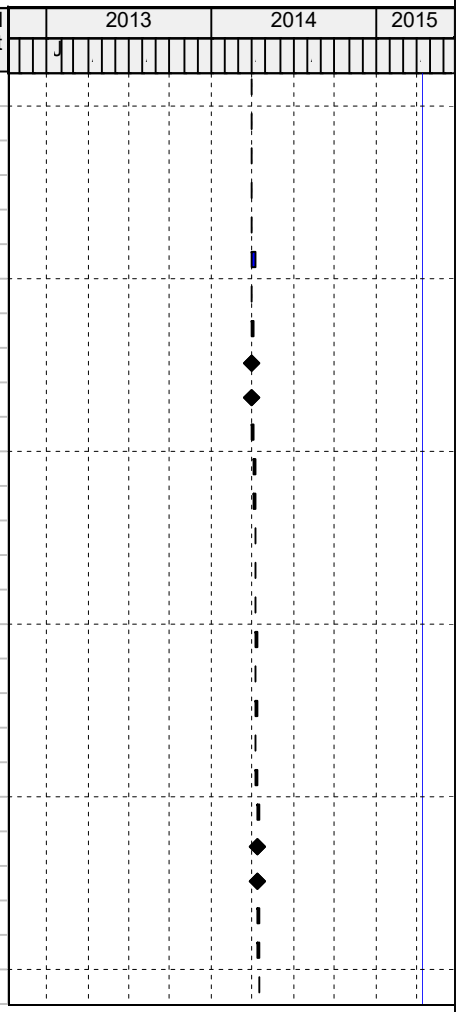



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P28-2014 | Stress Tendons | 1 | 0 | 17-Apr-14 A | 17-Apr-14 A | |
| P29-2000 | Strip Core | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| P27-2016 | Strip / ReShore Deck | 3 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L15-2018 | Remove Reshores | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| P28-2016 | Strip / ReShore Deck | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L15-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L16-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-May-14 A | 19-May-14 A | |
| L16-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2019 | Grind Ceiling for Skim Coat | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| **Ballroom Catwalk & Roof** | | | | | | |
| PC-2100 | Erect Structural Steel @ Porte Cochere | 3 | 0 | 30-Jan-14 A | 03-Feb-14 A | |
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 7 | 0 | 07-Feb-14 A | 17-Feb-14 A | |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| PC-2102 | Metal Decking @ Porte Cochere/ Roof | 2 | 0 | 17-Apr-14 A | 18-Apr-14 A | |
| BR-2112 | BR - Fireproofing @ Structural Steel | 2 | 0 | 27-May-14 A | 30-May-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Mech Penthouse** | | | | | | |
| PH-8706 | Set Mech Equipment @ Tower Roof | 3 | 0 | 22-May-14 A | 28-May-14 A | |
| PH-8708 | Set Equipment @ Penthouse | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| PH-8700 | PH - Structural Steel and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| **Vertical Circulation** | | | | | | |
| **Stairs** | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 25-Nov-13 A | 26-Nov-13 A | |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 27-Nov-13 A | 03-Dec-13 A | |
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 04-Dec-13 A | 05-Dec-13 A | |

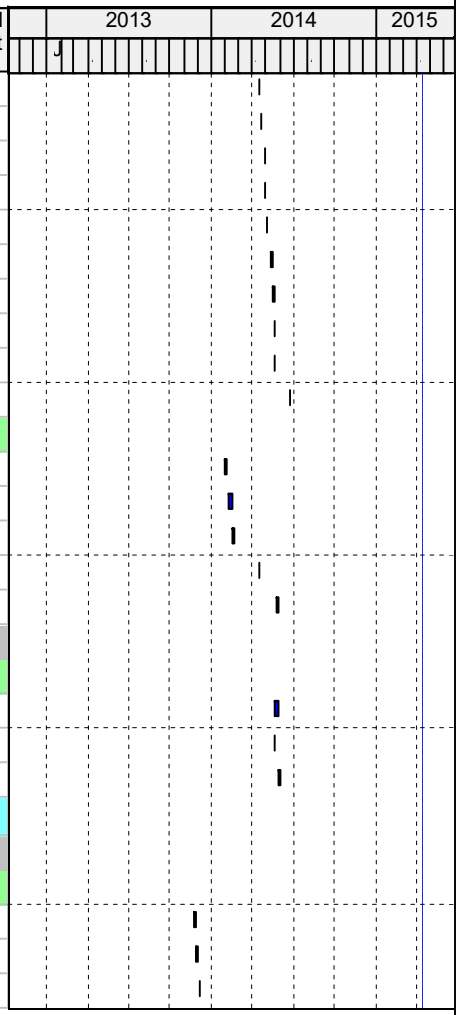


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 06-Dec-13 A | 09-Dec-13 A | |
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 2 | 0 | 03-Feb-14 A | 04-Feb-14 A | |
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 2 | 0 | 06-Feb-14 A | 07-Feb-14 A | |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 2 | 0 | 07-Feb-14 A | 07-Feb-14 A | |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 2 | 0 | 07-Feb-14 A | 10-Feb-14 A | |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 2 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 2 | 0 | 06-Mar-14 A | 07-Mar-14 A | |
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 2 | 0 | 07-Mar-14 A | 10-Mar-14 A | |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 2 | 0 | 13-Mar-14 A | 14-Mar-14 A | |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 2 | 0 | 08-Apr-14 A | 21-Apr-14 A | |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| S1-4040 | Stair 1 - Set Mtl Stairs / Railings L18 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 10-Dec-13 A | 11-Dec-13 A | |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 12-Dec-13 A | 13-Dec-13 A | |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 16-Dec-13 A | 17-Dec-13 A | |
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 18-Dec-13 A | 19-Dec-13 A | |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 2 | 0 | 12-Feb-14 A | 13-Feb-14 A | |
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 2 | 0 | 13-Feb-14 A | 13-Feb-14 A | |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 2 | 0 | 13-Feb-14 A | 14-Feb-14 A | |
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |

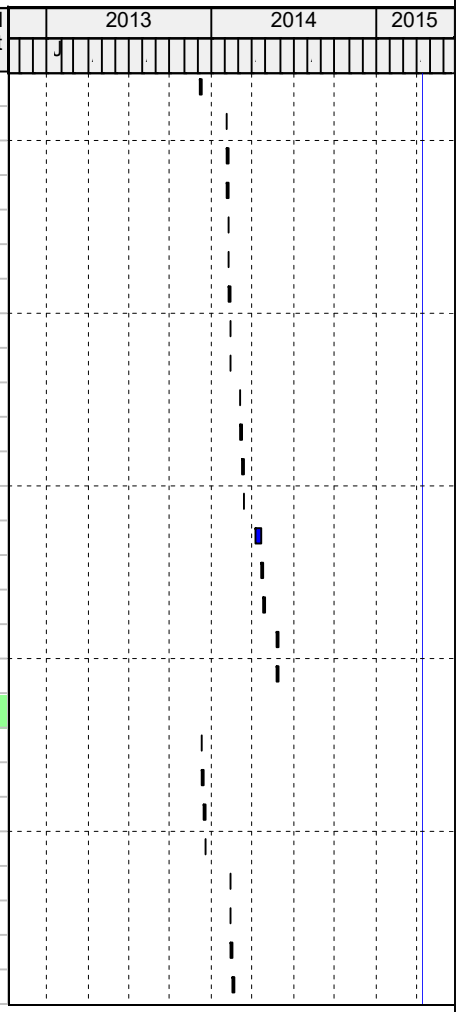



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 2 | 0 | 19-Feb-14 A | 20-Feb-14 A | |
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 2 | 0 | 21-Feb-14 A | 24-Feb-14 A | |
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 2 | 0 | 19-Mar-14 A | 20-Mar-14 A | |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 2 | 0 | 21-Mar-14 A | 22-Mar-14 A | |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 2 | 0 | 14-May-14 A | 15-May-14 A | |
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 2 | 0 | 16-May-14 A | 19-May-14 A | |
| S2-4038 | Stair 2 - Set Mtl Stairs / Railings L17 | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - Set Metal Stairs / Railings LL2 | 6 | 0 | 05-Mar-14 A | 20-Mar-14 A | |
| S3-4002 | Stair 3 - Set Metal Stairs / Railings LL1 | 6 | 0 | 17-Mar-14 A | 21-Mar-14 A | |
| S3-4004 | Stair 3 - Paint walls & railings | 4 | 4 | 06-May-15 | 11-May-15 | 1 |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |
| S4-4000 | Stair 4 - Set Metal Stairs / Railings LL2 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4002 | Stair 4 - Set Metal Stairs / Railings LL1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4004 | Stair 4 -Set Metal Stairs / Railings L1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4006 | Stair 4 - Paint walls & railings | 4 | 4 | 17-Apr-15 | 22-Apr-15 | 12 |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |
| S6-4000 | Stair 6 - Set Metal Stairs / Railings | 5 | 0 | 25-Jun-14 A | 01-Jul-14 A | |
| S6-4002 | Stair 6 - Paint walls & railings | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 20 |
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |

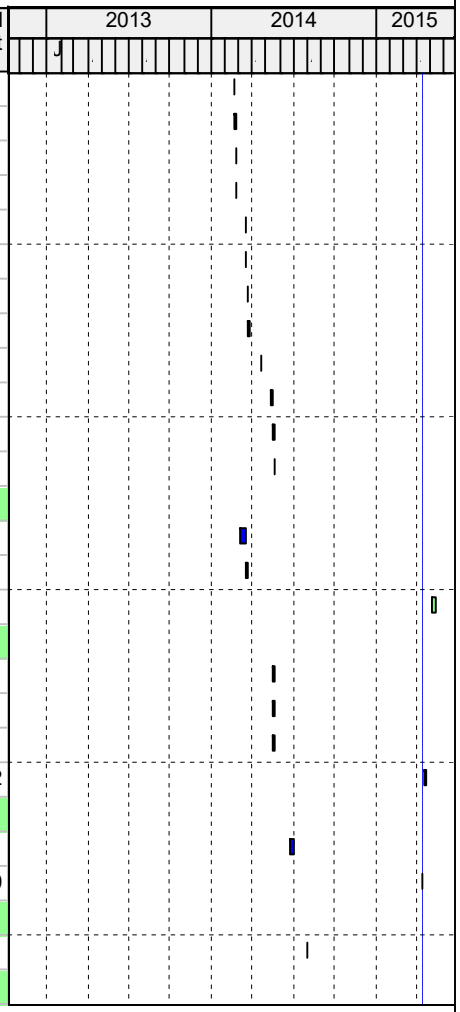



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes (DE | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a -Set Metal Stairs / Railings L1 | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| S4a-4002 | Stair 4a - Paint walls & railings | 2 | 2 | 23-Apr-15 | 24-Apr-15 | 12 |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 07-Jun-13 A | | |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 0 | 17-Jun-13 A | 21-Jun-13 A | |
| EL-1004 | Elev - Submittal Approval | 21 | 0 | 21-Jun-13 A | 01-Jan-14 A | |
| EL-1006 | Elev - Release to Manufacturing | 14 | 0 | 02-Jan-14 A | 15-Jan-14 A | |
| EL-1008 | Elev - Fabrication (Engineered Geared) | 95 | 0 | 16-Jan-14 A | 14-Jun-14 A | |
| EL-1010 | Elev - Machines delivered | 1 | 0 | 12-May-14 A | 12-May-14 A | |
| EL-1011 | Elev - Elevator Machines Flown & Set At Top Of Hoist | 5 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5016 | Elev 5 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-1216 | Elev 1&2 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-3416 | Elev 3&4 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-1202 | Elev 1&2 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-3402 | Elev 3&4 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-5018 | Elev 5 - Set Hoistway Machines | 3 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| EL-1218 | Elev 1&2 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-3418 | Elev 3&4 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-1200 | Elev 1&2 - Hoistway Clear & Ready (GC) | 0 | 0 | 20-Jun-14 A | | |
| EL-1204 | Elev 1&2 - Install Rails & Brackets | 17 | 0 | 23-Jun-14 A | 15-Jul-14 A | |
| EL-3400 | Elev 3&4 - Hoistway Clear & Ready (GC) | 0 | 0 | 23-Jun-14 A | | |
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 24-Jun-14 A | | |

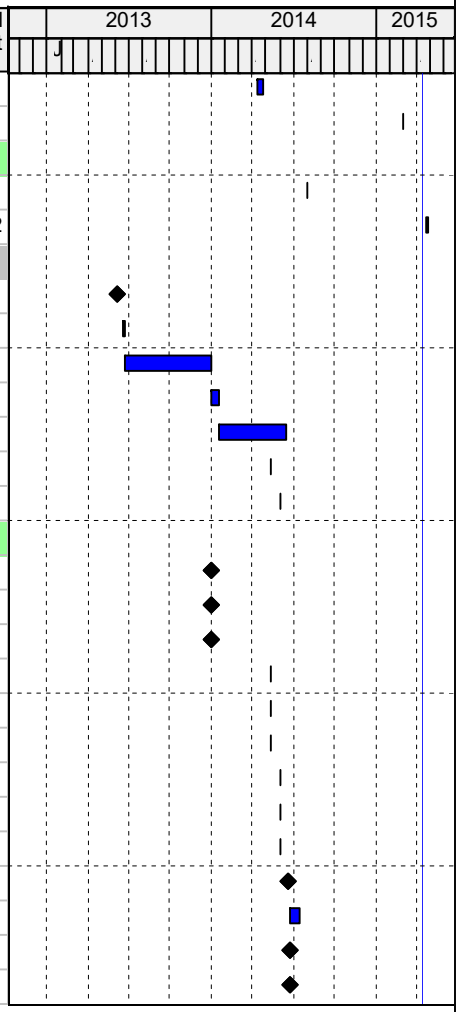



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-1206 | Elev 1&2 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Jul-14 A | |
| EL-1207 | Elev 1&2 - Install Pit Equipment/Car Sling/CWT Fram | 3 | 0 | 15-Jul-14 A | 01-Aug-14 A | |
| EL-1208 | Elev 1&2 - Install MHoist & Cable | 5 | 0 | 16-Jul-14 A | 24-Jul-14 A | |
| EL-3407 | Elev 3&4 - Install Pit Equipment/Car Sling/CWT Fram | 5 | 0 | 16-Jul-14 A | 06-Aug-14 A | |
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 21-Jul-14 A | | |
| EL-5004 | Elev 5 - Install Rails & Brackets | 13 | 0 | 21-Jul-14 A | 11-Aug-14 A | |
| EL-3404 | Elev 3&4 - Install Rails & Brackets | 18 | 0 | 23-Jul-14 A | 04-Aug-14 A | |
| EL-3406 | Elev 3&4 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 28-Jul-14 A | |
| EL-3408 | Elev 3&4 - Install Hoist & Cable | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| EL-5007 | Elev 5 - Install Pit Equipment/Car Sling/CWT Frame/V | 5 | 0 | 12-Aug-14 A | 15-Aug-14 A | |
| EL-1210 | Elev 1&2 - Install Entrances/Doors/Fixtures/Fascia | 19 | 0 | 14-Aug-14 A | 22-Sep-14 A | |
| EL-3410 | Elev 3&4 - Install Entrances/Doors/Fixtures/Fascia | 30 | 0 | 14-Aug-14 A | 02-Oct-14 A | |
| EL-5006 | Elev 5 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Aug-14 A | |
| EL-5008 | Elev 5 - Install MHoist & Cable | 4 | 0 | 18-Aug-14 A | 20-Aug-14 A | |
| EL-5010 | Elev 5 - Install Entrances/Doors/Fixtures/Fascia | 21 | 0 | 21-Aug-14 A | 26-Sep-14 A | |
| EL-1212 | Elev 1&2 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 22-Sep-14 A | 13-Oct-14 A | |
| EL-5012 | Elev 5 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 26-Sep-14 A | 16-Oct-14 A | |
| EL-3412 | Elev 3&4 - Install Hoistway Equipment/Pipe & Wire | 23 | 0 | 03-Oct-14 A | 03-Nov-14 A | |
| EL-1214 | Elev 1&2 - Install Cab/Wiring/Door Operator(s) | 11 | 0 | 14-Oct-14 A | 28-Oct-14 A | |
| EL-5014 | Elev 5 - Install Cab/Wiring/Door Operator(s) | 7 | 0 | 17-Oct-14 A | 27-Oct-14 A | |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 1 | 0 | 24-Oct-14 A | 24-Oct-14 A | |
| EL-6016 | Elev 6 - Hoistway Walls Complete (GC) | 0 | 0 | | 24-Oct-14 A | |
| EL-6004 | Elev 6 - Install Cylinders/Rails & Brackets | 4 | 0 | 27-Oct-14 A | 30-Oct-14 A | |
| EL-5022 | Elev 5 - Adjust | 5 | 0 | 28-Oct-14 A | 03-Nov-14 A | |
| EL-1222 | Elev 1&2 - Adjust | 5 | 0 | 29-Oct-14 A | 04-Nov-14 A | |
| EL-6006 | Elev 6 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 30-Oct-14 A | |
| EL-6007 | Elev 6 - Install Pit Equipment/Car Sling | 2 | 0 | 31-Oct-14 A | 03-Nov-14 A | |

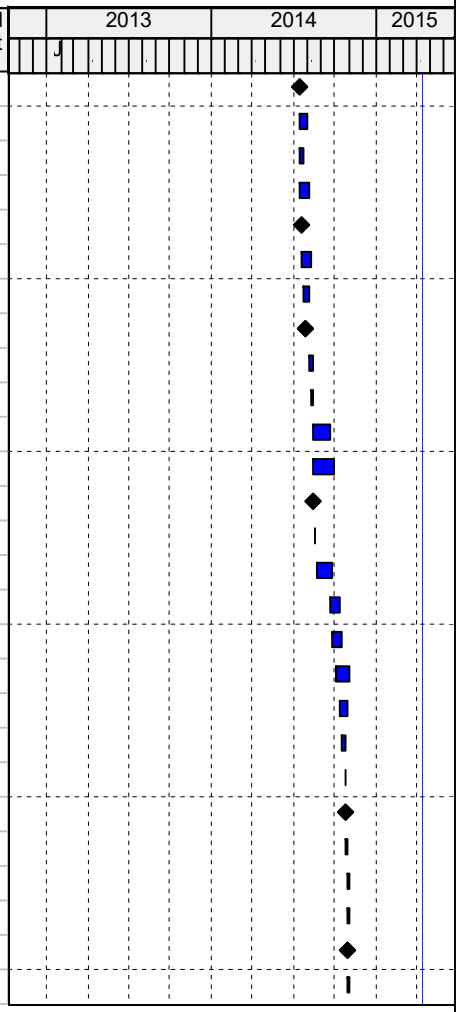



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| EL-3414 | Elev 3&4 - Install Cab/Wiring/Door Operator(s) | 10 | 0 | 04-Nov-14 A | 17-Nov-14 A | |
| EL-6018 | Elev 6 - Install Machine Room Equipment | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| EL-1224 | Elev 1&2 - Clean / Paint / Punchlist | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| EL-5026 | Elev 5 - Inspections | 7 | 0 | 13-Nov-14 A | 14-Nov-14 A | |
| EL-3422 | Elev 3&4 - Adjust | 8 | 0 | 18-Nov-14 A | 20-Nov-14 A | |
| EL-6012 | Elev 6 - Install hoistway rails & divider beams | 2 | 0 | 20-Nov-14 A | 21-Nov-14 A | |
| EL-6010 | Elev 6 - Install elevator fronts/rears | 9 | 0 | 09-Dec-14 A | 24-Dec-14 A | |
| EL-6014 | Elev 6 - Cab build-out | 5 | 0 | 15-Dec-14 A | 30-Jan-15 A | |
| EL-6022 | Elev 6 - Final cleaning at EMR | 4 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| EL-1226 | Elev 1&2 - CoB/L&I Inspections (for FF&E use) | 3 | 0 | 04-Mar-15 A | 06-Mar-15 A | |
| EL-3424 | Elev 3&4 - Walsh/TKE pre-inspection | 6 | 0 | 27-Mar-15 A | 27-Mar-15 A | |
| EL-3426 | Elev 3&4 - CoB/L&I Inspections (Final) | 5 | 5 | 13-Apr-15 | 17-Apr-15 | 12 |
| EL-6024 | Elev 6 - Walsh/TKE pre-inspection | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 15 |
| EL-6026 | Elev 6 - CoB/L&I Inspections (Final) | 5 | 5 | 20-Apr-15 | 24-Apr-15 | 12 |
| **Exterior Shell** | | | | | | |
| **Elevations** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2** | | | | | | |
| L3D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Feb-14 A | 12-Feb-14 A | |
| L3-5308 | L3- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 17-Feb-14 A | 21-Feb-14 A | |
| L4D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Feb-14 A | 19-Feb-14 A | |
| L4-5308 | L4- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Feb-14 A | 28-Feb-14 A | |
| L5D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Feb-14 A | 26-Feb-14 A | |
| L5-5308 | L5- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 03-Mar-14 A | 07-Mar-14 A | |
| L6D5308 | Deliver/Stock Wall Panels | 1 | 0 | 05-Mar-14 A | 05-Mar-14 A | |
| L6-5308 | L6- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |

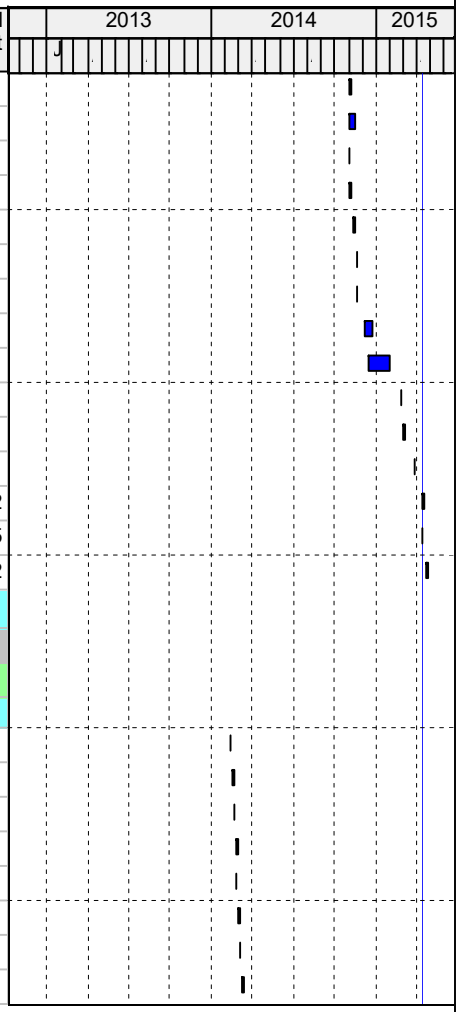



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L7-5308 | L7- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L7D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Mar-14 A | 12-Mar-14 A | |
| L8D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Mar-14 A | 19-Mar-14 A | |
| L8-5308 | L8- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Mar-14 A | 28-Mar-14 A | |
| L9D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L9-5308 | L9- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 31-Mar-14 A | 07-Apr-14 A | |
| 10D5308 | Deliver/Stock Wall Panels | 1 | 0 | 02-Apr-14 A | 02-Apr-14 A | |
| L10-5308 | L10- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 07-Apr-14 A | 11-Apr-14 A | |
| 11D5308 | Deliver/Stock Wall Panels | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L11-5308 | L11- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 11-Apr-14 A | 18-Apr-14 A | |
| 12D5308 | Deliver/Stock Wall Panels | 1 | 0 | 16-Apr-14 A | 16-Apr-14 A | |
| L12-5308 | L12- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Apr-14 A | 25-Apr-14 A | |
| 14D5308 | Deliver/Stock Wall Panels | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L14-5308 | L14 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Apr-14 A | 01-May-14 A | |
| 15D5308 | Deliver/Stock Wall Panels | 1 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L15-5308 | L15 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| 16D5308 | Deliver/Stock Wall Panels | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L16-5308 | L16- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| 17D5308 | Deliver/Stock Wall Panels | 1 | 0 | 14-May-14 A | 14-May-14 A | |
| L17-5308 | L17 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 20-May-14 A | 11-Jun-14 A | |
| LL2-5308 | LL2 Thru L4 - Support Frame/Sheathing for Metal Wa | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL1-5308 | LL1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| L1-5308 | L1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| **Level 1** | | | | | | |
| L3-5102 | L3- Storefront Frames | 7 | 0 | 18-Aug-14 A | 29-Sep-14 A | |
| L1-5102 | L1 - Storefront Frames (excl. Main Entry Facade) | 8 | 0 | 02-Sep-14 A | 11-Sep-14 A | |
| L1-5104 | L1 - Storefront Glazing (excl. Main Entry Facade) | 4 | 0 | 19-Sep-14 A | 24-Sep-14 A | |

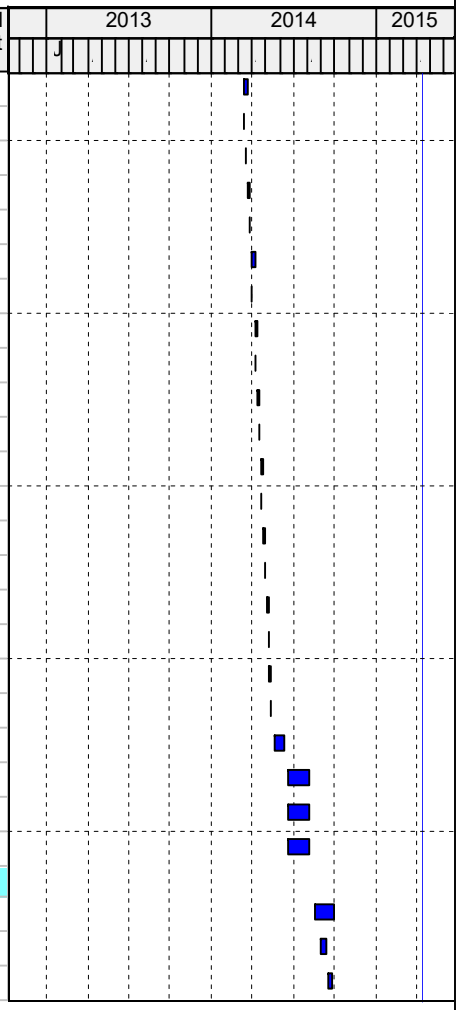


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EP-5110 | L1 - Revolving Doors | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L3-5104 | L3 - Storefront Glazing | 3 | 0 | 30-Sep-14 A | 03-Oct-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Levels 3-4** | | | | | | |
| L3-5130 | L3 - Install Punch Windows | 5 | 0 | 24-Feb-14 A | 10-Mar-14 A | |
| L4-5130 | L4 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 12-Mar-14 A | |
| L5-5130 | L5 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L6-5130 | L6- Install Punch Windows | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L7-5130 | L7 - Install Punch Windows | 5 | 0 | 18-Mar-14 A | 21-Mar-14 A | |
| L8-5130 | L8 - Install Punch Windows | 5 | 0 | 24-Mar-14 A | 28-Mar-14 A | |
| L9-5130 | L9 - Install Punch Windows | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L10-5130 | L10 - Install Punch Windows | 5 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-5130 | L11 - Install Punch Windows | 5 | 0 | 14-Apr-14 A | 21-Apr-14 A | |
| L12-5130 | L12 - Install Punch Windows | 5 | 0 | 22-Apr-14 A | 25-Apr-14 A | |
| L14-5130 | L14 - Install Punch Windows | 5 | 0 | 28-Apr-14 A | 05-May-14 A | |
| L15-5130 | L15 - Install Punch Windows | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| L16-5130 | L16 - Install Punch Windows | 5 | 0 | 12-May-14 A | 20-May-14 A | |
| L17-5130 | L17 - Install Punch Windows | 5 | 0 | 27-May-14 A | 16-Jun-14 A | |
| **Roofs** | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| RF-4026 | L1 - City Park - Protection Board | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| **Pool Membrane - (elev 18')** | | | | | | |
| RF-4034 | Pool - Install plumbing | 3 | 0 | 20-Oct-14 A | 22-Oct-14 A | |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |
| RF-4010 | AR - Set Mechanical Equipment | 5 | 0 | 10-Jun-14 A | 12-Jun-14 A | |

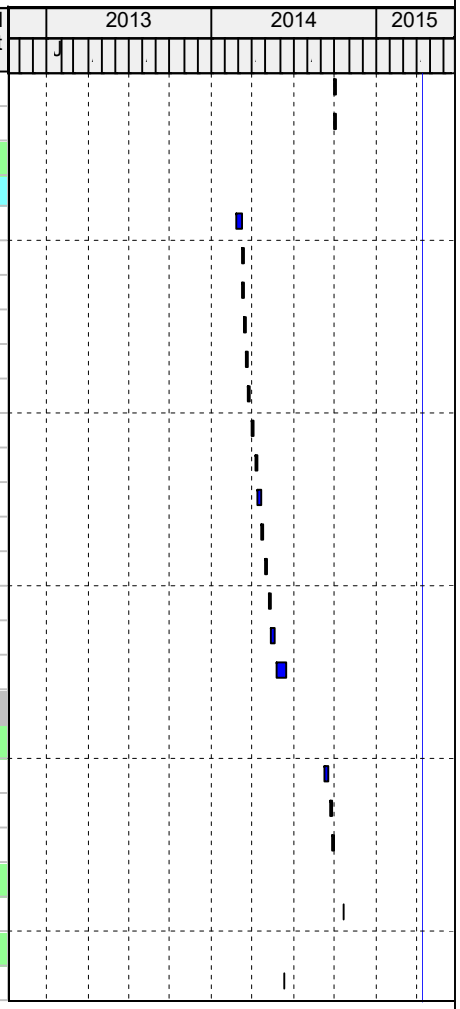



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 10 | 0 | 04-Aug-14 A | 27-Aug-14 A | |
| RF-4012 | L2.5 Horseshoe - Install corrugated metal panels | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 8 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |
| PC-4008 | RF - Entry / Porte Cochere Roofing System | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | RF - Upper Ballroom Roofing System | 3 | 0 | 28-Jul-14 A | 31-Jul-14 A | |
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 4 | 0 | 31-Jul-14 A | 04-Aug-14 A | |
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |
| RF-4018 | TR - Terrace Roof - Green Roofing System | 5 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| RF-4020 | TR - Terrace Roof - Install sheet metal capping[DELE | 1 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4022 | TR - Terrace Roof - Install deocrative metal railing | 5 | 5 | 27-Apr-15 | 01-May-15 | 3 |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Perimeter Framing / Sul | 10 | 0 | 02-Jun-14 A | 08-Jul-14 A | |
| RF-4002 | Tower Roof - Roofing System | 10 | 0 | 20-Aug-14 A | 17-Sep-14 A | |
| **PH - Roof - (elev 173')** | | | | | | |
| RF-4030 | PH - Roofing System | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| RF-4032 | PH - Coping / Flashing [DELETED] | 3 | 0 | 01-Sep-14 A | 01-Sep-14 A | |
| **Rough-In's** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6002 | LL4 - Layout | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| LL4-6008 | LL4 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL4-6012 | LL4 - Fire Sprinkler Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6014 | LL4 - Plumbing Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |

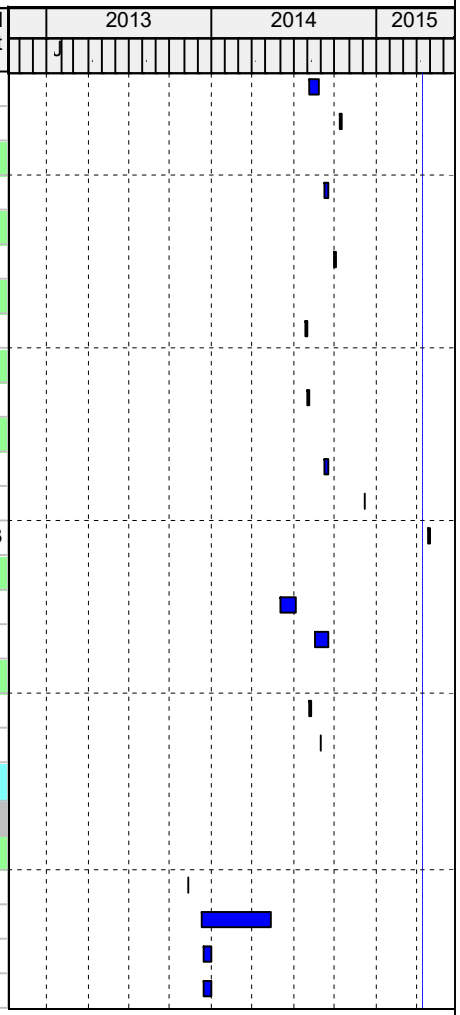



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-6018 | LL4 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6004 | LL4 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL4-6016 | LL4 - Electrical RI | 10 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties RI | 8 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6010 | LL4 - Elevator pits | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| LL4-6020 | LL4 - H Mtl Frames | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL4-6024 | LL4 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6002 | LL3 - Layout | 1 | 0 | 19-Nov-13 A | 19-Nov-13 A | |
| LL3-6008 | LL3 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL3-6012 | LL3 - Fire Sprinkler RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6014 | LL3 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6018 | LL3 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6004 | LL3 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL3-6020 | LL3 - H Mtl Frames | 3 | 0 | 08-May-14 A | 09-May-14 A | |
| LL3-6010 | LL3 - F/P Curbs | 5 | 0 | 19-May-14 A | 19-May-14 A | |
| LL3-6016 | LL3 - Electrical RI | 2 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties RI | 8 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL3-6024 | LL3 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6002 | LL2 - Layout | 1 | 0 | 14-Jan-14 A | 14-Jan-14 A | |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| LL2-6012 | LL2 - Fire Sprinkler RI | 10 | 0 | 21-Jan-14 A | 03-Feb-14 A | |
| LL2-6014 | LL2 - Plumbing RI | 10 | 0 | 21-Jan-14 A | 14-Feb-14 A | |
| LL2E-6016 | LL2 - Electrical RI | 8 | 0 | 03-Feb-14 A | 17-Mar-14 A | |

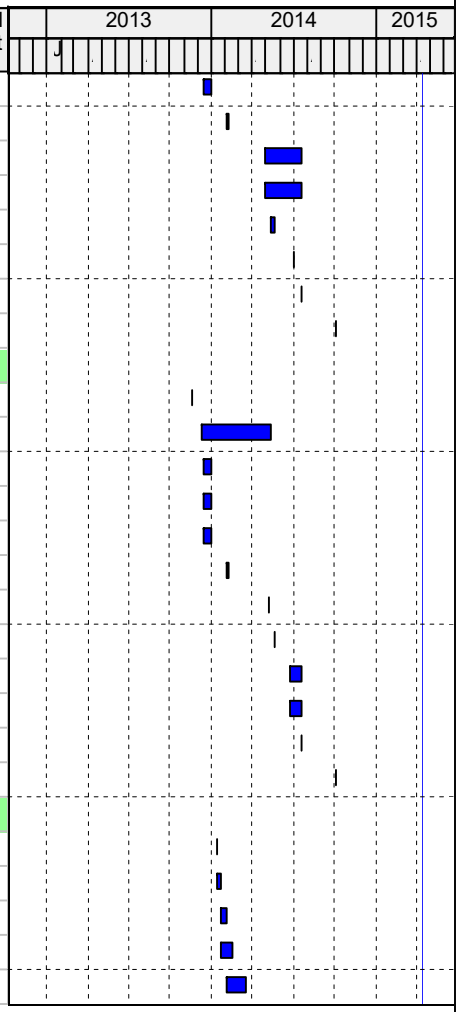



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-6016 | LL2 - Electrical RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2-6018 | LL2 - HVAC RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2–6004 | LL2 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL2E-6004 | LL2 - CMU Walls | 10 | 0 | 04-Mar-14 A | 09-May-14 A | |
| LL2E-6012 | LL2 - Fire Sprinkler RI | 8 | 0 | 21-Mar-14 A | 01-Apr-14 A | |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 24-Apr-14 A | |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 3 | 0 | 23-Apr-14 A | 21-Jul-14 A | |
| LL2E-6020 | LL2 - H Mtl Frames | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| LL2-6020 | LL2 - H Mtl Frames | 3 | 0 | 12-May-14 A | 13-May-14 A | |
| LL2E-6008 | LL2 - Int Wall Framing | 5 | 0 | 13-May-14 A | 22-Jun-14 A | |
| LL2E-6014 | LL2 - Plumbing RI | 8 | 0 | 13-May-14 A | 30-May-14 A | |
| LL2E-6018 | LL2 - HVAC RI | 8 | 0 | 13-May-14 A | 04-Aug-14 A | |
| LL2E-6022 | LL2 - Fire Alarm / Elec Specialties RI (East of 10) | 8 | 0 | 13-May-14 A | 22-Sep-14 A | |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties RI (West of 10) | 8 | 0 | 19-May-14 A | 22-Sep-14 A | |
| LL2-6015 | LL2 - Main Elect Room Set Equip / RI - Power to Ma | 15 | 0 | 30-Jun-14 A | 26-Sep-14 A | |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 0 | 16-Jul-14 A | 21-Jul-14 A | |
| LL2-6024 | LL2 - Inspections | 2 | 0 | 15-Sep-14 A | 03-Oct-14 A | |
| LL2-6010 | F/P Curbs at Garage | 3 | 3 | 27-Apr-15 | 29-Apr-15 | 4 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6002 | Layout | 3 | 0 | 03-Jan-14 A | 08-Jan-14 A | |
| LL1-6008 | Int Wall Framing & Inspection | 6 | 0 | 08-Jan-14 A | 21-Jul-14 A | |
| LL1-Z2-6002 | Layout | 3 | 0 | 08-Jan-14 A | 14-Jan-14 A | |
| LL1-Z3-6002 | Layout | 3 | 0 | 14-Jan-14 A | 17-Jan-14 A | |
| LL1-Z2-6008 | Int Wall Framing & Inspection | 6 | 0 | 17-Jan-14 A | 01-Aug-14 A | |
| LL1-Z3-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-Jan-14 A | 04-Aug-14 A | |
| LL1-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 09-May-14 A | |

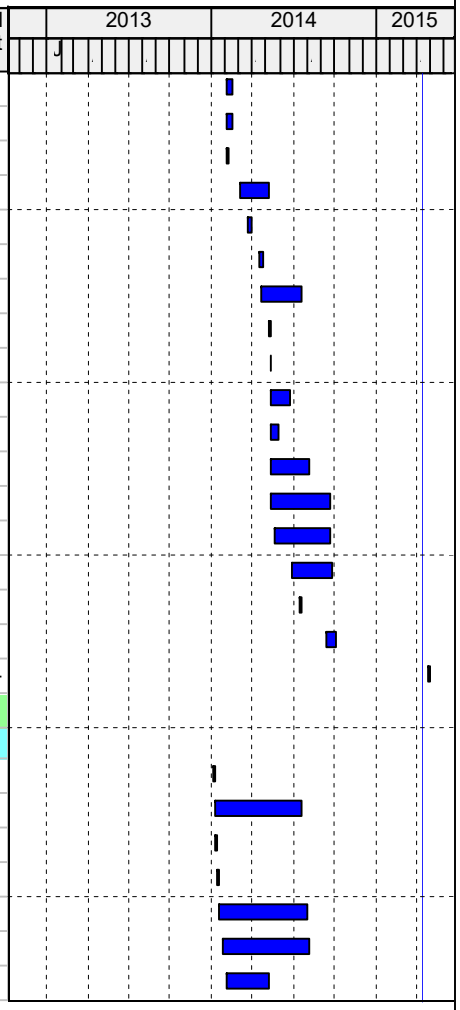


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 28-Apr-14 A | |
| LL1-Z3-6004 | CMU Walls (At All Areas North of Q-Line) | 3 | 0 | 03-Feb-14 A | 13-May-14 A | |
| LL1C-6012 | Complete Fire Sprinkler RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6016 | Complete Electrical RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 10 | 0 | 17-Feb-14 A | 16-Sep-14 A | |
| LL1C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 30-Apr-14 A | |
| LL1-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-Z2-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z2-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z3-6012 | Fire Sprinkler RI (At All Areas North of Q-Line) | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z3-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 11-Sep-14 A | |
| LL1-Z3-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z2C-6012 | Complete Fire Sprinkler RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6014 | Complete Plumbing RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6016 | Complete Electrical RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 15 | 0 | 24-Feb-14 A | 15-Sep-14 A | |
| LL1-Z2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2-6020 | Hollow Metal Door Frames | 5 | 0 | 17-Mar-14 A | 04-Apr-14 A | |

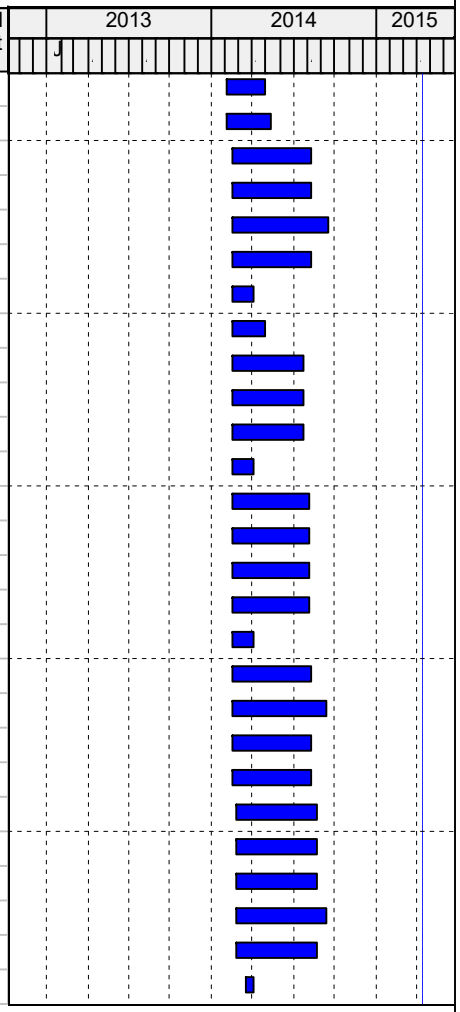



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| LL1-Z3-6020 | Hollow Metal Door Frames (At All Areas North of Q-Lir | 1 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| L1B-6004 | CMU Walls [including East Service Corridor] | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L1L-6002 | Layout [including back of house] | 3 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 29-Apr-14 A | |
| L1B-6008 | Int Wall Framing & Inspection | 6 | 0 | 21-Apr-14 A | 08-Aug-14 A | |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 5 | 0 | 25-Apr-14 A | 21-Jul-14 A | |
| LL1C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L1K-6004 | CMU Walls [including public restroom] | 3 | 0 | 05-May-14 A | 08-May-14 A | |
| L1K-6002 | Layout [including public restroom] | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| L1K-6008 | Int Wall Framing & Inspection | 4 | 0 | 09-May-14 A | 22-Aug-14 A | |
| L1B-6002 | Layout [including East Service Corridor] | 3 | 0 | 14-May-14 A | 27-May-14 A | |
| L1L-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-May-14 A | 06-Oct-14 A | |
| L1L-6004 | CMU Walls [including back of house] | 3 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L1K-6012 | Fire Sprinkler RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6014 | Plumbing RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6016 | Electrical RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1K-6018 | HVAC RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1B-6014 | Plumbing RI [including East Service Corridor] | 10 | 0 | 16-Jun-14 A | 24-Jun-14 A | |
| L1B-6018 | HVAC RI | 10 | 0 | 20-Jun-14 A | 15-Aug-14 A | |
| L1B-6012 | Fire Sprinkler RI | 10 | 0 | 21-Jun-14 A | 15-Aug-14 A | |
| L1L-6018 | HVAC RI | 5 | 0 | 23-Jun-14 A | 13-Oct-14 A | |
| L1L-6014 | Plumbing RI | 5 | 0 | 24-Jun-14 A | 28-Oct-14 A | |
| L1L-6010 | CMU Seismic Clips [including back of house] [DELET | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1L-6012 | Fire Sprinkler RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |
| L1L-6016 | Electrical RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |
| L1L-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 27-Jun-14 A | 13-Oct-14 A | |

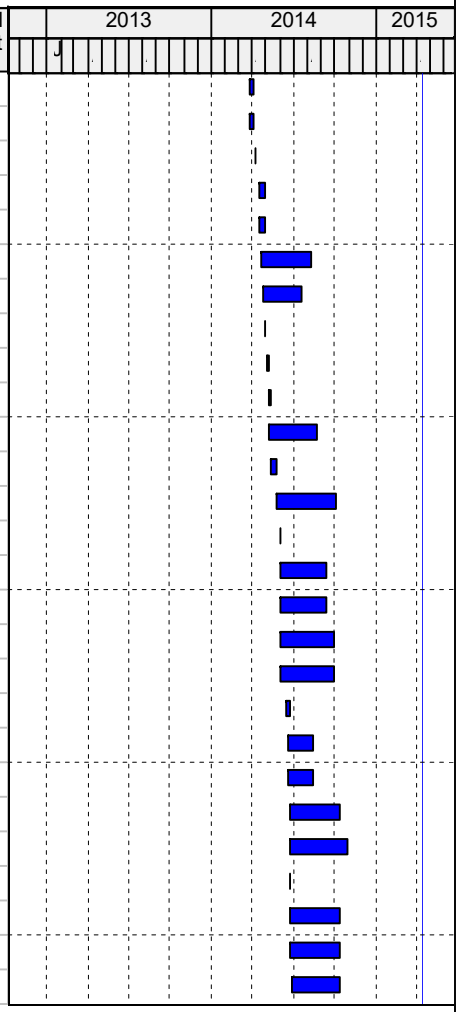



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 27-Jun-14 A | 29-Sep-14 A | |
| LL1-Z3-6009 | Frame Ceilings [DELETED] | 4 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1B-6016 | Electrical RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| L1B-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| LL1-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-Z2-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L1B-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-6024 | Inspections for Cover | 1 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L1B-6020 | Hollow Metal Door Frames | 5 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| LL1-Z3-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L1K-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 06-Aug-14 A | |
| LL1-Z2-6024 | Inspections for Cover | 2 | 0 | 07-Aug-14 A | 08-Aug-14 A | |
| L1K-6020 | Hollow Metal Door Frames | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-Z2-6009 | Frame Ceilings & Inspection | 6 | 0 | 22-Aug-14 A | 13-Oct-14 A | |
| L1L-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Aug-14 A | 13-Oct-14 A | |
| LL1-6009 | Frame Ceilings & Inspection (except for bar redesign | 9 | 0 | 02-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3-6024 | Inspections for Cover | 2 | 0 | 12-Sep-14 A | 12-Sep-14 A | |
| LL1-Z3C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6016 | Complete Electrical RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3C-6018 | Complete HVAC RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| L1KC-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 4 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L1B-6024 | Inspections for Cover (Main Ballroom N/S/W Walls & | 3 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1K-6024 | Inspections for Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1KC-6014 | Complete Plumbing RI @ Ceilings & Inspection | 4 | 0 | 02-Oct-14 A | 07-Oct-14 A | |
| L1BC-6014 | Complete Plumbing RI @ Ceilings | 7 | 0 | 06-Oct-14 A | 08-Oct-14 A | |

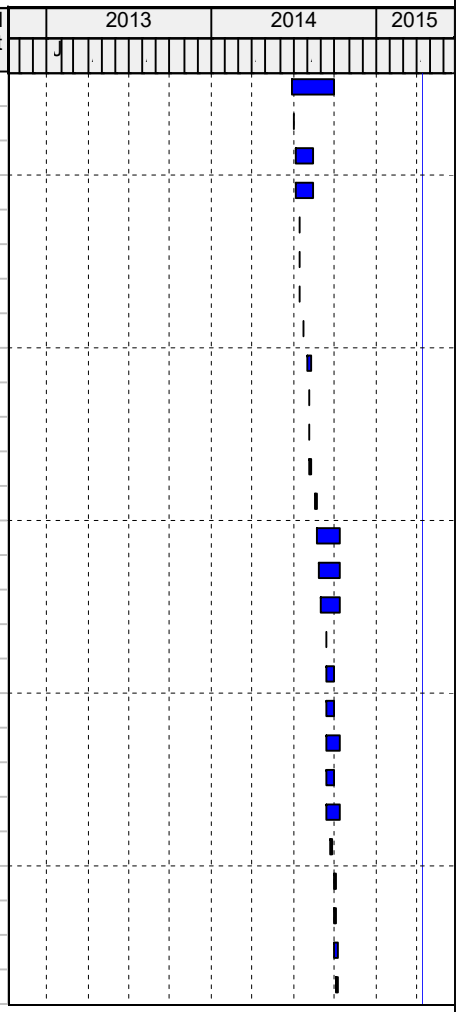



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1KC-6018 | Complete HVAC RI @ Ceilings & Inspection | 4 | 0 | 06-Oct-14 A | 10-Nov-14 A | |
| L1KC-6016 | Complete Electrical RI @ Ceilings & Inspection | 3 | 0 | 20-Oct-14 A | 10-Nov-14 A | |
| L1KC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 3 | 0 | 20-Oct-14 A | 10-Nov-14 A | |
| L1L-6024 | Inspections for Cover | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L1L-6009 | Frame ceilings & inspection at high ceiling | 13 | 0 | 24-Nov-14 A | 20-Jan-15 A | |
| L1B-6009 | Frame Ceilings & inspection at Main Ballroom (per re | 5 | 0 | 04-Dec-14 A | 16-Jan-15 A | |
| L1LC-6012 | Complete fire sprinkler RI @ ceilings | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1LC-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| L1LC-6016 | Complete electrical rough-in @ ceilings & inspection | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1LC-6018 | Complete HVAC RI @ Ceilings | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1LC-6022 | Complete fire alarm/elec specialties RI @ ceilings & ir | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1K-6009 | Frame ceilings & inspection at public restroom | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L1B-8118 | Lighting & electrical trim at Ballrooms | 7 | 5 | 07-Apr-15 A | 17-Apr-15 | 6 |
| L1B-8112 | Fire sprinkler trim at Ballrooms | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 9 |
| L1B-8204 | HVAC trim at Ballrooms | 5 | 5 | 13-Apr-15 | 17-Apr-15 | 6 |
| L1BC-6022 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 9 |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 0 | 17-Apr-14 A | 09-May-14 A | |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6006 | L2 - Support Frame/Sheathing for Metal Panels | 6 | 0 | 23-Apr-14 A | 07-Aug-14 A | |
| L02-6008 | L2 - Int Wall Framing | 10 | 0 | 25-Apr-14 A | 17-Jul-14 A | |
| L02-6014 | L2 - Plumbing RI | 15 | 0 | 28-Apr-14 A | 07-Aug-14 A | |
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 0 | 28-Apr-14 A | 09-May-14 A | |
| L02-6004 | L2 - CMU Walls | 5 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L02-6002 | L2 - Layout | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L02-6018 | L2 - HVAC RI (including equipment) | 20 | 0 | 18-Jun-14 A | 10-Sep-14 A | |

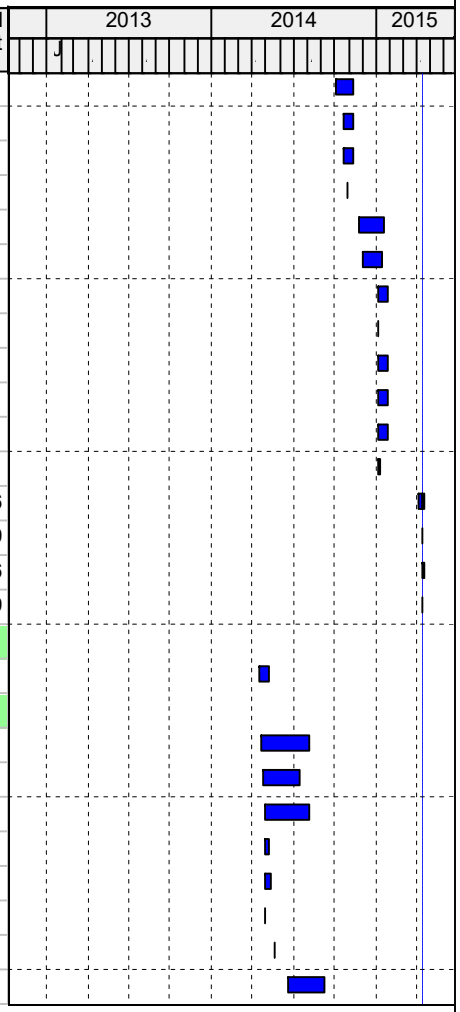



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-6016 | L2 - Electrical RI | 10 | 0 | 24-Jun-14 A | 14-Aug-14 A | |
| L02-6022 | L2 - Fire Alarm / Elec Specialties RI | 10 | 0 | 24-Jun-14 A | 10-Oct-14 A | |
| L02-6012 | L2 - Fire Sprinkler RI | 10 | 0 | 26-Jun-14 A | 07-Aug-14 A | |
| L02-6020 | L2 - H Mtl Frames | 5 | 0 | 11-Jul-14 A | 17-Jul-14 A | |
| L02-6024 | L2 - Inspections - North Half | 2 | 0 | 10-Oct-14 A | 20-Oct-14 A | |
| Upper Tower - (Levels 3 thru PH) | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L04-6012 | Fire Sprinkler Mains | 5 | 0 | 01-Feb-14 A | 03-Apr-14 A | |
| L03-8219 | HVAC Risers | 5 | 0 | 11-Feb-14 A | 23-Mar-14 A | |
| L03-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 11-Feb-14 A | 03-Mar-14 A | |
| L03-6002 | Layout | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| L04-8219 | HVAC Risers | 5 | 0 | 13-Feb-14 A | 23-Mar-14 A | |
| L05-8219 | HVAC Risers | 5 | 0 | 17-Feb-14 A | 03-Mar-14 A | |
| L03-6008 | Frame Shaft Walls | 3 | 0 | 18-Feb-14 A | 26-Mar-14 A | |
| L04-6002 | Layout | 5 | 0 | 19-Feb-14 A | 25-Feb-14 A | |
| L04-6008 | Frame Shaft Walls | 3 | 0 | 20-Feb-14 A | 26-Mar-14 A | |
| L03-6011 | PreRock Shafts | 2 | 0 | 24-Feb-14 A | 25-Mar-14 A | |
| L03-6010 | Frame Walls | 5 | 0 | 25-Feb-14 A | 25-Mar-14 A | |
| L05-6002 | Layout | 5 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| L04-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 28-Feb-14 A | 05-Mar-14 A | |
| L03-6016 | Electrical RI | 5 | 0 | 03-Mar-14 A | 04-Apr-14 A | |
| L03-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 12-Mar-14 A | |
| L04-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 13-Mar-14 A | |
| L04-6010 | Frame Walls | 5 | 0 | 04-Mar-14 A | 05-Jun-14 A | |
| L05-6008 | Frame Shaft Walls | 3 | 0 | 05-Mar-14 A | 27-Mar-14 A | |
| L06-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L07-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |

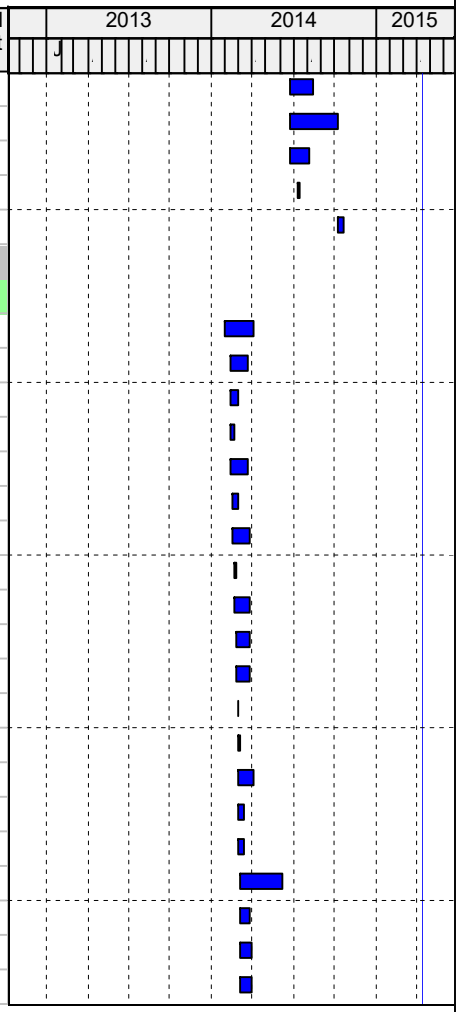



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 06-Mar-14 A | 21-Mar-14 A | |
| L03-6020 | Install Hollow Metal Frames | 3 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L04-6020 | Install Hollow Metal Frames | 3 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L05-6010 | Frame Walls | 5 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L06-6002 | Layout | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L04-6011 | PreRock Shafts | 2 | 0 | 18-Mar-14 A | 25-Mar-14 A | |
| L05-6009 | Inspect Shafts | 1 | 0 | 18-Mar-14 A | 18-Mar-14 A | |
| L05-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| L06-6008 | Frame Shaft Walls | 3 | 0 | 19-Mar-14 A | 03-Apr-14 A | |
| L06-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 27-Mar-14 A | |
| L04-6016 | Electrical RI | 5 | 0 | 20-Mar-14 A | 09-Apr-14 A | |
| L05-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 26-Mar-14 A | |
| L06-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 07-Apr-14 A | |
| L07-6002 | Layout | 5 | 0 | 24-Mar-14 A | 30-Apr-14 A | |
| L03-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L03-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L05-6016 | Electrical RI | 5 | 0 | 25-Mar-14 A | 05-Jun-14 A | |
| L04-6019 | Complete Top Out GWB | 2 | 0 | 26-Mar-14 A | 06-Jun-14 A | |
| L05-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L06-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| L03-6019 | Complete Top Out GWB | 2 | 0 | 27-Mar-14 A | 02-May-14 A | |
| L08-6002 | Layout | 5 | 0 | 27-Mar-14 A | 02-Apr-14 A | |
| L05-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 28-Mar-14 A | 03-Apr-14 A | |
| L06-6010 | Frame Walls | 5 | 0 | 28-Mar-14 A | 07-Apr-14 A | |
| L03-6012 | Fire Sprinkler Mains | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |

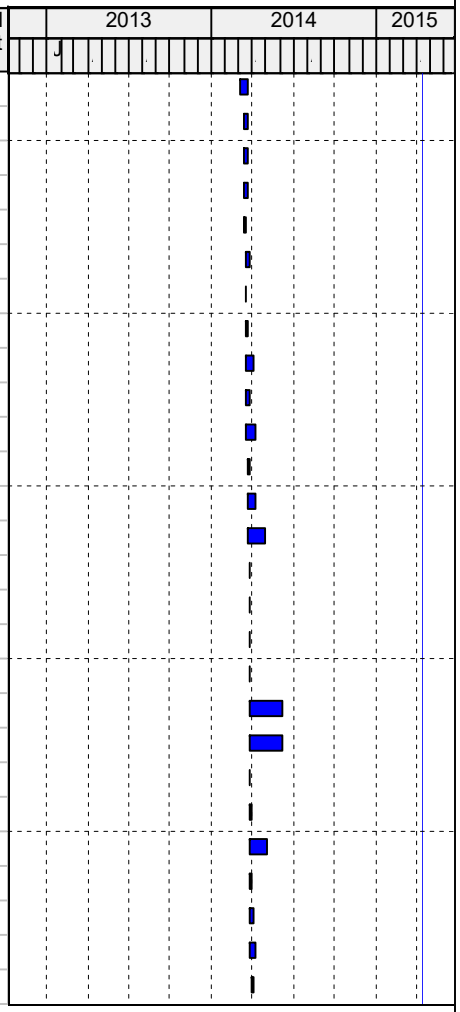



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6008 | Frame Shaft Walls | 3 | 0 | 31-Mar-14 A | 03-Apr-14 A | |
| L05-6019 | Complete Top Out GWB | 2 | 0 | 01-Apr-14 A | 08-Apr-14 A | |
| L07-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 01-Apr-14 A | 11-Apr-14 A | |
| L08-6008 | Frame Shaft Walls | 3 | 0 | 02-Apr-14 A | 21-Apr-14 A | |
| L03-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L04-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L05-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L06-6016 | Electrical RI | 5 | 0 | 03-Apr-14 A | 15-Apr-14 A | |
| L07-6009 | Inspect Shafts | 1 | 0 | 03-Apr-14 A | 03-Apr-14 A | |
| L07-6011 | PreRock Shafts | 2 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| L05-6012 | Fire Sprinkler Mains | 5 | 0 | 04-Apr-14 A | 30-Apr-14 A | |
| L06-6012 | Fire Sprinkler Mains | 5 | 0 | 07-Apr-14 A | 30-Apr-14 A | |
| L06-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L06-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L07-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| L07-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L03-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L03-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L04-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L06-6009 | Inspect Shafts | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L06-6019 | Complete Top Out GWB | 2 | 0 | 08-Apr-14 A | 18-Apr-14 A | |
| L07-6010 | Frame Walls | 5 | 0 | 08-Apr-14 A | 15-Apr-14 A | |
| L08-6011 | PreRock Shafts | 2 | 0 | 08-Apr-14 A | 23-Apr-14 A | |
| L09-6002 | Layout | 5 | 0 | 08-Apr-14 A | 26-Apr-14 A | |
| L03-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 09-Apr-14 A | 08-May-14 A | |
| L03-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L05-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 09-Apr-14 A | 14-Apr-14 A | |

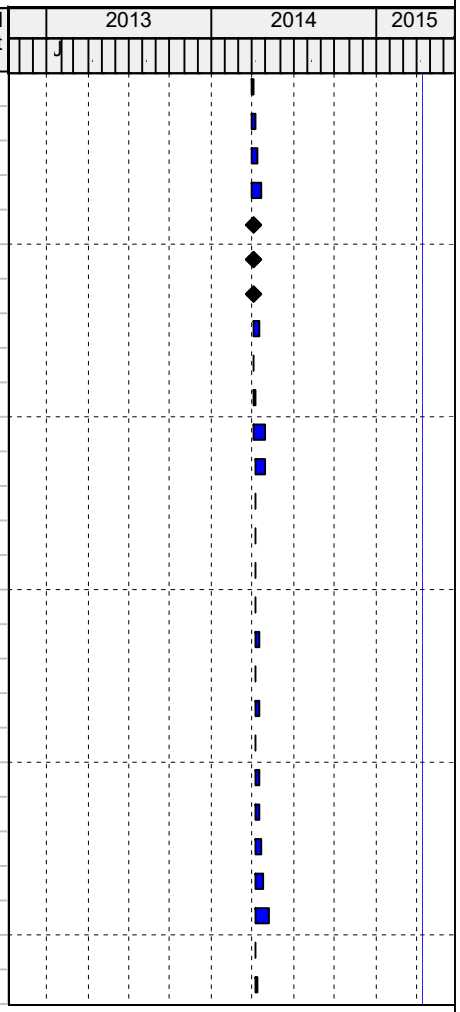



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-6009 | Inspect Shafts | 1 | 0 | 09-Apr-14 A | 25-Apr-14 A | |
| L09-6008 | Frame Shaft Walls | 3 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| L08-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| L04-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 15-Apr-14 A | 16-Apr-14 A | |
| L07-6012 | Fire Sprinkler Mains | 5 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| L07-6016 | Electrical RI | 5 | 0 | 15-Apr-14 A | 12-May-14 A | |
| L07-6020 | Install Hollow Metal Frames | 3 | 0 | 16-Apr-14 A | 23-Apr-14 A | |
| L05-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 17-Apr-14 A | 25-Apr-14 A | |
| L06-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 17-Apr-14 A | 12-May-14 A | |
| L06-6023 | Inspection of Exterior Framing | 0 | 0 | 17-Apr-14 A | | |
| L09-8219 | HVAC Risers | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L09-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L04-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 18-Apr-14 A | 20-Apr-14 A | |
| L04-6028 | PreRock at Heat Pumps | 2 | 0 | 20-Apr-14 A | 22-Apr-14 A | |
| L08-8219 | HVAC Risers | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6009 | Inspect Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6011 | PreRock Shafts | 2 | 0 | 22-Apr-14 A | 24-Apr-14 A | |
| L04-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L06-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 23-Apr-14 A | 25-Apr-14 A | |
| L08-6020 | Install Hollow Metal Frames | 3 | 0 | 23-Apr-14 A | 13-May-14 A | |
| L11-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L11-8220 | Plumbing Risers - Install | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L04-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L09-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L10-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |

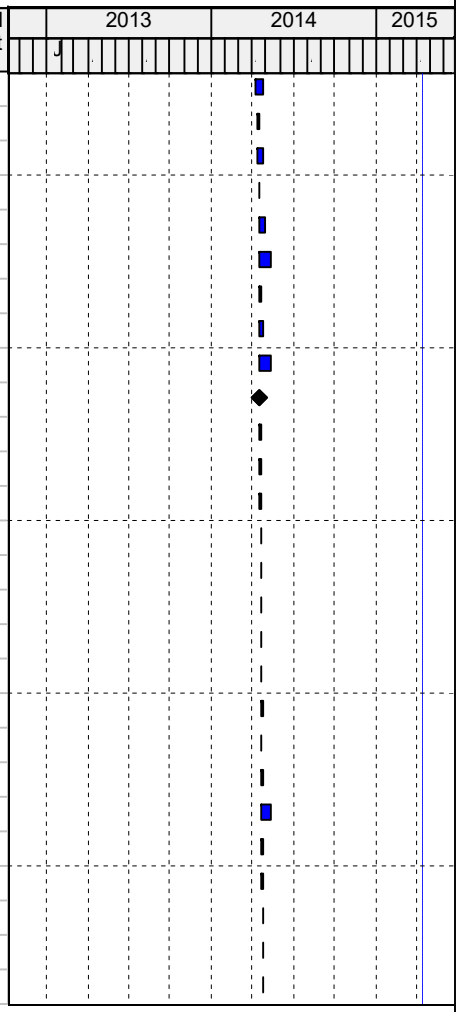



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 20-May-14 A | |
| L12-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L04-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 25-Apr-14 A | 11-Jun-14 A | |
| L04-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L09-6010 | Frame Walls | 5 | 0 | 25-Apr-14 A | 20-May-14 A | |
| L09-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L10-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L11-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 30-Apr-14 A | |
| L12-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L08-6010 | Frame Walls | 5 | 0 | 26-Apr-14 A | 30-Apr-14 A | |
| L10-6002 | Layout | 5 | 0 | 27-Apr-14 A | 27-Apr-14 A | |
| L04-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 28-Apr-14 A | 30-Apr-14 A | |
| L05-6018 | HVAC RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6028 | PreRock at Heat Pumps | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L07-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 28-Apr-14 A | 12-May-14 A | |
| L10-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-Apr-14 A | 22-May-14 A | |
| L11-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L12-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L05-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| L05-6028 | PreRock at Heat Pumps | 2 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L06-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 09-May-14 A | |

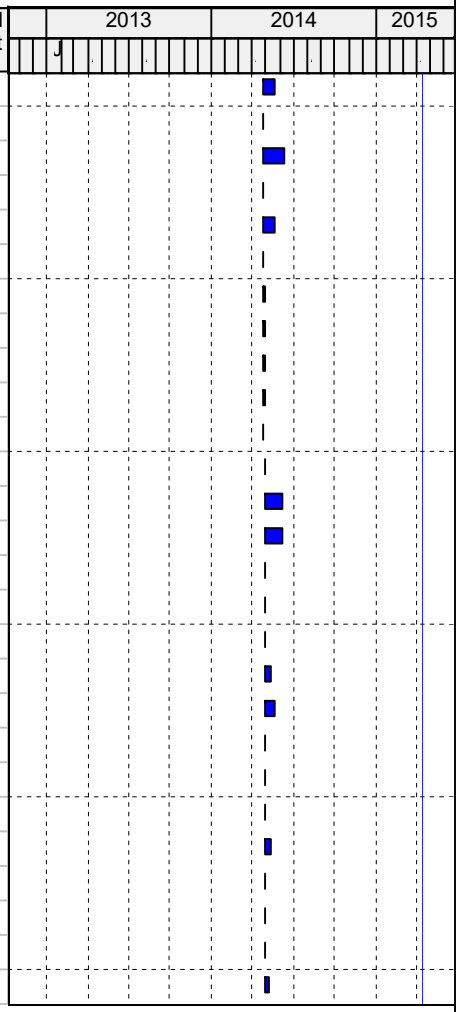



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L06-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L08-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L08-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L09-6020 | Install Hollow Metal Frames | 3 | 0 | 29-Apr-14 A | 20-May-14 A | |
| L09-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L10-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L04-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 30-Apr-14 A | 02-May-14 A | |
| L09-6019 | Complete Top Out GWB | 2 | 0 | 30-Apr-14 A | 06-Jun-14 A | |
| L11-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L12-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L03-6028 | PreRock at Heat Pumps | 2 | 0 | 01-May-14 A | 02-May-14 A | |
| L05-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L06-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L03-6014 | Set Tubs & Plumbing RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L05-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L05-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| L06-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L06-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 09-May-14 A | |
| L03-6018 | HVAC RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L03-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 06-May-14 A | 06-May-14 A | |
| L07-6014 | Set Tubs & Plumbing RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L07-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 06-May-14 A | 09-May-14 A | |

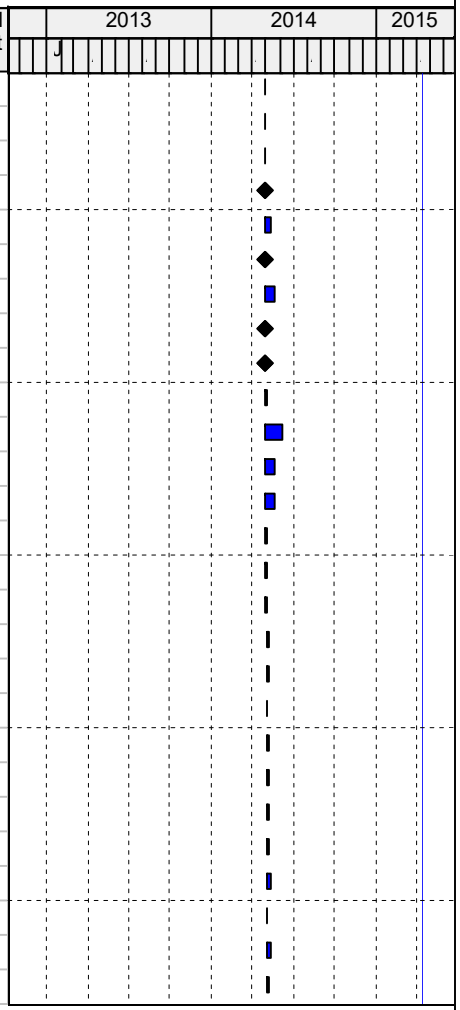



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6004 | CMU Wall/Clips | 3 | 0 | 07-May-14 A | 08-May-14 A | |
| L03-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L03-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 08-May-14 A | 13-May-14 A | |
| L03-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6004 | CMU Walls | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6018 | HVAC RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L11-6010 | Frame Walls | 5 | 0 | 09-May-14 A | 15-May-14 A | |
| L05-6014 | Set Tubs & Plumbing RI | 5 | 0 | 12-May-14 A | 05-Jun-14 A | |
| L07-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 12-May-14 A | 13-May-14 A | |
| L11-6020 | Install Hollow Metal Frames | 3 | 0 | 12-May-14 A | 14-May-14 A | |
| L11-6019 | Complete Top Out GWB | 2 | 0 | 12-May-14 A | 14-May-14 A | |
| L14-6002 | Layout | 5 | 0 | 12-May-14 A | 14-May-14 A | |
| L15-6002 | Layout | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L05-6004 | CMU Walls | 3 | 0 | 13-May-14 A | 13-May-14 A | |
| L06-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 25-Jun-14 A | |
| L06-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 13-May-14 A | 14-Jul-14 A | |
| L07-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 05-Jun-14 A | |
| L07-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| L07-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 13-May-14 A | 13-May-14 A | |
| L14-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L16-6002 | Layout | 5 | 0 | 13-May-14 A | 16-May-14 A | |
| L06-6004 | CMU Walls | 3 | 0 | 14-May-14 A | 14-May-14 A | |
| L07-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 15-May-14 A | |
| L08-6012 | Fire Sprinkler Mains | 5 | 0 | 15-May-14 A | 20-May-14 A | |

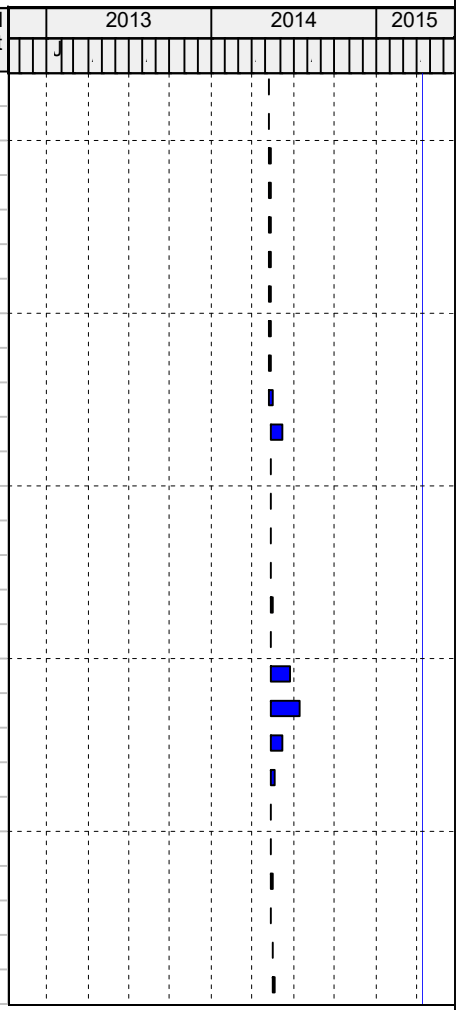



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6002 | Layout | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L07-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 16-May-14 A | 25-Jun-14 A | |
| L08-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L11-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L12-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L07-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L08-6028 | PreRock at Heat Pumps | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L09-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L10-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L11-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L15-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 19-May-14 A | 19-May-14 A | |
| L07-6028 | PreRock at Heat Pumps | 2 | 0 | 20-May-14 A | 21-May-14 A | |
| L07-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L08-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 20-May-14 A | 21-May-14 A | |
| L10-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L11-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L14-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L07-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 21-May-14 A | 27-May-14 A | |
| L08-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L08-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |

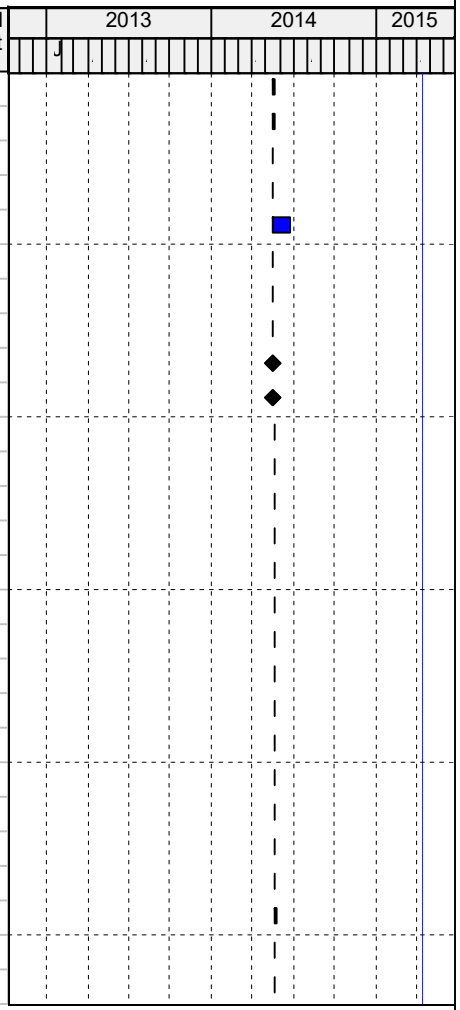



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6028 | PreRock at Heat Pumps | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L10-6014 | Set Tubs & Plumbing RI | 5 | 0 | 21-May-14 A | 27-Jun-14 A | |
| L10-6010 | Frame Walls | 5 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6019 | Complete Top Out GWB | 2 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L11-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L12-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L14-8220 | Plumbing Risers - Install | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L15-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L16-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L07-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| L08-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 22-May-14 A | 22-May-14 A | |
| L10-6012 | Fire Sprinkler Mains | 5 | 0 | 22-May-14 A | 27-May-14 A | |
| L08-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L09-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6020 | Install Hollow Metal Frames | 3 | 0 | 23-May-14 A | 03-Jun-14 A | |
| L10-6028 | PreRock at Heat Pumps | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L14-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L15-8220 | Plumbing Risers - Install | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L09-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 27-May-14 A | 27-May-14 A | |
| L12-6010 | Frame Walls | 5 | 0 | 27-May-14 A | 02-Jun-14 A | |
| L08-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L09-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 28-May-14 A | 28-May-14 A | |
| L10-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 28-May-14 A | 03-Jun-14 A | |
| L14-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L15-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-May-14 A | 30-May-14 A | |
| L16-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 28-May-14 A | 28-May-14 A | |

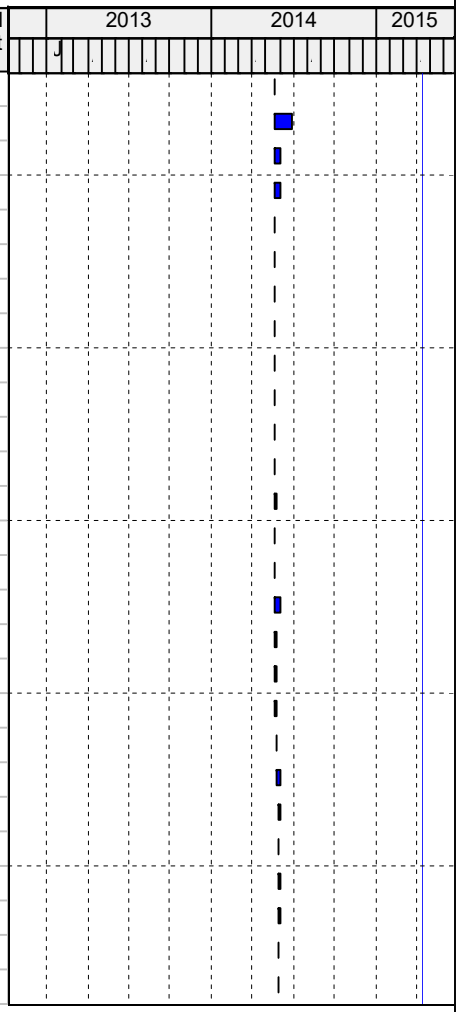



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8220 | Plumbing Risers - Install | 2 | 0 | 28-May-14 A | 29-May-14 A | |
| L08-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 29-May-14 A | 30-May-14 A | |
| L10-6016 | Electrical RI | 5 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L10-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| L12-6012 | Fire Sprinkler Mains | 5 | 0 | 30-May-14 A | 26-Jun-14 A | |
| L12-6020 | Install Hollow Metal Frames | 3 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L15-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L17-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L17-8220 | Plumbing Risers - Install | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L10-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L11-6016 | Electrical RI | 5 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L11-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L12-6019 | Complete Top Out GWB | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L14-6020 | Install Hollow Metal Frames | 3 | 0 | 02-Jun-14 A | 05-Jun-14 A | |
| L14-6010 | Frame Walls | 5 | 0 | 02-Jun-14 A | 04-Jun-14 A | |
| L16-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| L14-6019 | Complete Top Out GWB | 2 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L16-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L10-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| L17-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 04-Jun-14 A | 11-Jun-14 A | |
| L08-6016 | Electrical RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L08-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L09-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L12-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L15-6010 | Frame Walls | 3 | 0 | 05-Jun-14 A | 11-Jun-14 A | |

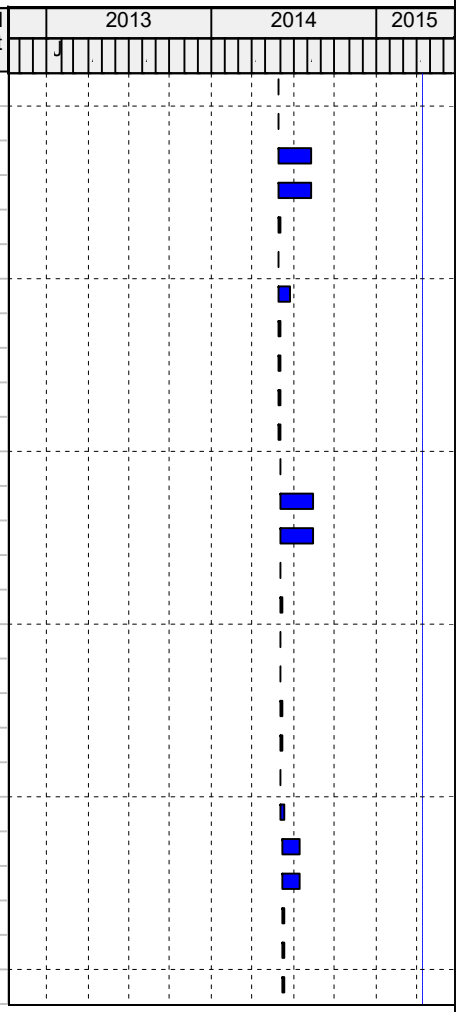



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6012 | Fire Sprinkler Mains | 5 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L09-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L11-6012 | Fire Sprinkler Mains | 4 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L12-6014 | Set Tubs & Plumbing RI | 4 | 0 | 06-Jun-14 A | 27-Jun-14 A | |
| L11-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jun-14 A | 11-Jun-14 A | |
| L09-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-Jun-14 A | 25-Jun-14 A | |
| L14-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L15-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L16-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L09-6016 | Electrical RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L14-6014 | Set Tubs & Plumbing RI | 4 | 0 | 10-Jun-14 A | 21-Jul-14 A | |
| L15-6020 | Install Hollow Metal Frames | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L15-6019 | Complete Top Out GWB | 2 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6014 | Set Tubs & Plumbing RI | 4 | 0 | 11-Jun-14 A | 26-Jun-14 A | |
| L11-6028 | PreRock at Heat Pumps | 2 | 0 | 13-Jun-14 A | 14-Jun-14 A | |
| L11-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 14-Jun-14 A | 14-Jun-14 A | |
| L14-6012 | Fire Sprinkler Mains | 2 | 0 | 16-Jun-14 A | 27-Jun-14 A | |
| L14-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 18-Jun-14 A | 18-Jun-14 A | |
| L15-6023 | Inspection of Exterior Framing | 0 | 0 | 18-Jun-14 A | | |
| L17-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 18-Jun-14 A | 23-Jun-14 A | |
| L17-6010 | Frame Walls | 5 | 0 | 18-Jun-14 A | 29-Jul-14 A | |
| L10-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L12-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-Jun-14 A | 19-Jun-14 A | |

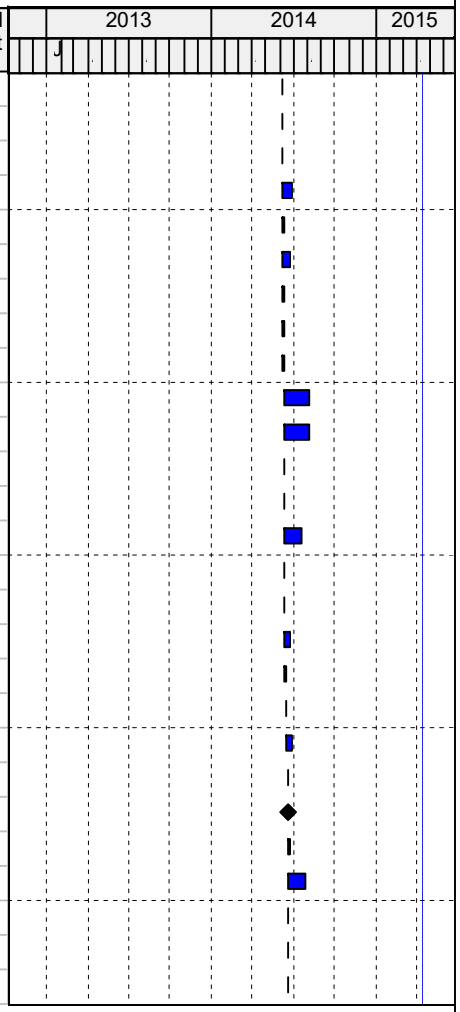



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6023 | Inspection of Exterior Framing | 0 | 0 | 20-Jun-14 A | | |
| L15-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-Jun-14 A | 20-Jun-14 A | |
| L10-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-Jun-14 A | 23-Jun-14 A | |
| L15-6014 | Set Tubs & Plumbing RI | 5 | 0 | 22-Jun-14 A | 24-Jul-14 A | |
| L08-6018 | HVAC RI | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L12-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L14-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L15-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L08-6221 | Frame Unit Ceilings | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| L11-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 24-Jun-14 A | 27-Jun-14 A | |
| L12-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L14-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6023 | Inspection of Exterior Framing | 0 | 0 | 24-Jun-14 A | | |
| L12-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| L12-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L14-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L15-6012 | Fire Sprinkler Mains | 2 | 0 | 25-Jun-14 A | 22-Jul-14 A | |
| L16-6023 | Inspection of Exterior Framing | 0 | 0 | 25-Jun-14 A | | |
| L03-6024 | Inspections for GWB Cover | 1 | 0 | 27-Jun-14 A | 27-Jun-14 A | |
| L09-6018 | HVAC RI | 3 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L09-6221 | Frame Unit Ceilings | 2 | 0 | 27-Jun-14 A | 30-Jun-14 A | |
| L12-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L14-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L15-6028 | PreRock at Heat Pumps | 2 | 0 | 30-Jun-14 A | 01-Jul-14 A | |
| L16-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 30-Jun-14 A | 30-Jun-14 A | |

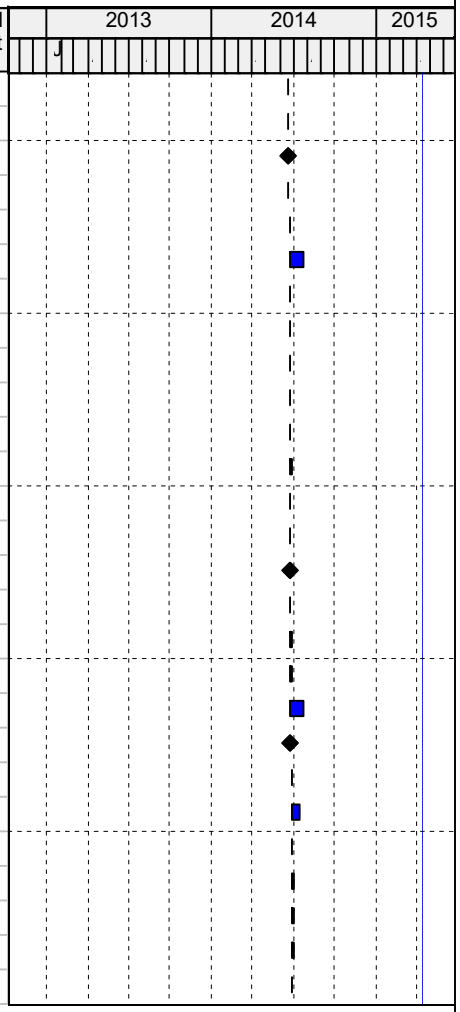



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6010 | Frame Walls | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| L16-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L15-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L15-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L04-6024 | Inspections for GWB Cover | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L10-6018 | HVAC RI | 3 | 0 | 07-Jul-14 A | 21-Jul-14 A | |
| L11-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L15-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L16-6012 | Fire Sprinkler Mains | 2 | 0 | 07-Jul-14 A | 24-Jul-14 A | |
| L16-6020 | Install Hollow Metal Frames | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L16-6028 | PreRock at Heat Pumps | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L17-6019 | Complete Top Out GWB | 1 | 0 | 07-Jul-14 A | 08-Aug-14 A | |
| L11-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L15-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 08-Jul-14 A | 04-Aug-14 A | |
| L17-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jul-14 A | 01-Aug-14 A | |
| L10-6221 | Frame Unit Ceilings | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| L17-6012 | Fire Sprinkler Mains | 2 | 0 | 09-Jul-14 A | 12-Aug-14 A | |
| L05-6024 | Inspections for GWB Cover | 2 | 0 | 10-Jul-14 A | 10-Jul-14 A | |
| L04-6000 | Tape/Finish GWB | 6 | 0 | 11-Jul-14 A | 23-Jul-14 A | |
| L16-6019 | Complete Top Out GWB | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L16-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L15-6018 | HVAC RI | 3 | 0 | 16-Jul-14 A | 18-Jul-14 A | |
| L16-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-6024 | Inspections for GWB Cover | 2 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6018 | HVAC RI | 3 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L16-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 21-Jul-14 A | 18-Aug-14 A | |

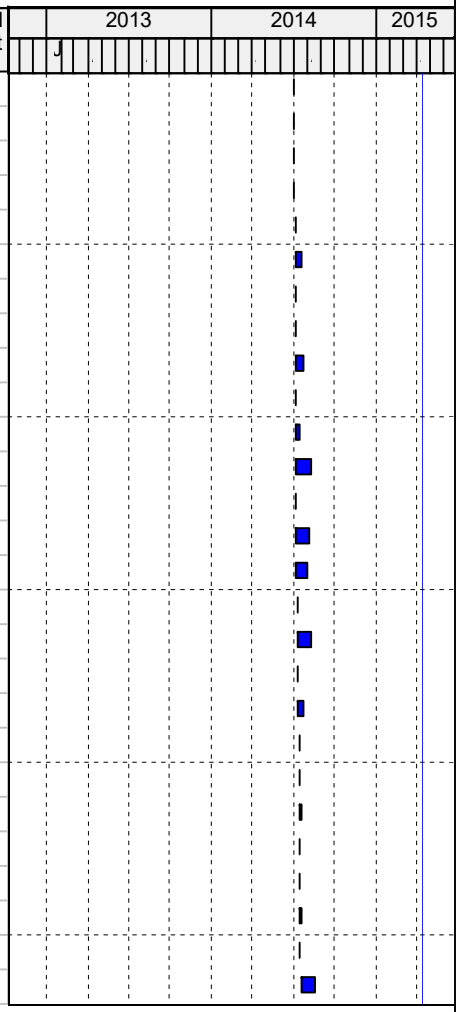



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6013 | Fire Sprinkler Branch Lines | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| L03-6000 | Tape/Finish GWB | 6 | 0 | 23-Jul-14 A | 29-Jul-14 A | |
| L11-6018 | HVAC RI | 3 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L15-6221 | Frame Unit Ceilings | 2 | 0 | 23-Jul-14 A | 01-Aug-14 A | |
| L16-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L17-6020 | Install Hollow Metal Frames | 3 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| L11-6221 | Frame Unit Ceilings | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L12-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L14-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L14-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L16-6014 | Set Tubs & Plumbing RI | 5 | 0 | 28-Jul-14 A | 18-Aug-14 A | |
| L07-6024 | Inspections for GWB Cover | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L12-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L05-6000 | Tape/Finish GWB | 6 | 0 | 31-Jul-14 A | 05-Aug-14 A | |
| L08-6024 | Inspections for GWB Cover | 2 | 0 | 31-Jul-14 A | 31-Jul-14 A | |
| L12-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L14-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L06-6000 | Tape/Finish GWB | 4 | 0 | 06-Aug-14 A | 11-Aug-14 A | |
| L09-6024 | Inspections for GWB Cover | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L07-6000 | Tape/Finish GWB | 5 | 0 | 07-Aug-14 A | 16-Aug-14 A | |
| L11-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 08-Aug-14 A | 14-Aug-14 A | |
| L17-6014 | Set Tubs & Plumbing RI | 5 | 0 | 08-Aug-14 A | 16-Sep-14 A | |

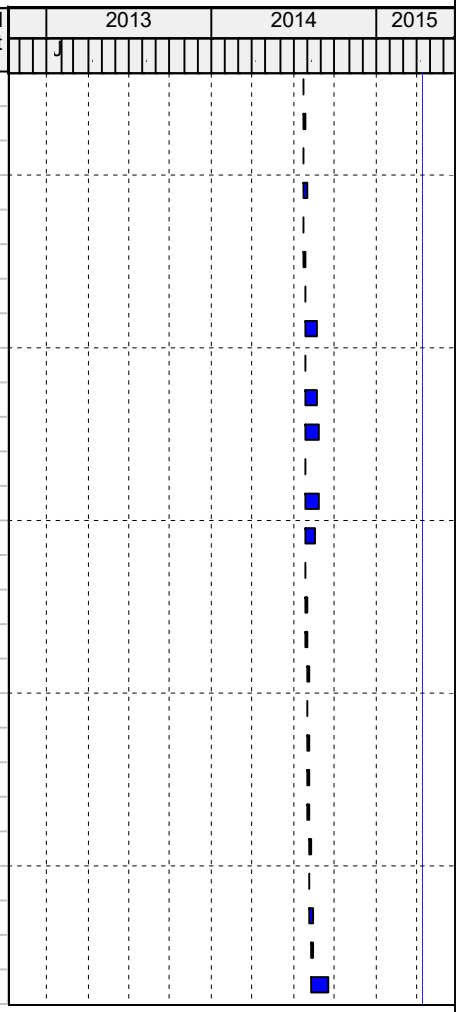



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-6024 | Inspections for GWB Cover | 2 | 0 | 11-Aug-14 A | 12-Aug-14 A | |
| L09-6000 | Tape/Finish GWB | 5 | 0 | 14-Aug-14 A | 19-Aug-14 A | |
| L08-6000 | Tape/Finish GWB | 5 | 0 | 16-Aug-14 A | 21-Aug-14 A | |
| L11-6024 | Inspections for GWB Cover | 2 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L16-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 18-Aug-14 A | 29-Aug-14 A | |
| L10-6000 | Tape/Finish GWB | 5 | 0 | 19-Aug-14 A | 23-Aug-14 A | |
| L16-6221 | Frame Unit Ceilings | 4 | 0 | 21-Aug-14 A | 26-Aug-14 A | |
| L17-6018 | HVAC RI | 3 | 0 | 21-Aug-14 A | 10-Sep-14 A | |
| L12-6024 | Inspections for GWB Cover | 2 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L15-6016 | Electrical RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L15-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L11-6000 | Tape/Finish GWB | 5 | 0 | 23-Aug-14 A | 29-Aug-14 A | |
| L17-6221 | Frame Unit Ceilings | 4 | 0 | 26-Aug-14 A | 28-Aug-14 A | |
| L14-6024 | Inspections for GWB Cover | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L16-6016 | Electrical RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L16-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L12-6000 | Tape/Finish GWB | 5 | 0 | 02-Sep-14 A | 08-Sep-14 A | |
| L15-6024 | Inspections for GWB Cover | 2 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L14-6000 | Tape/Finish GWB | 5 | 0 | 06-Sep-14 A | 11-Sep-14 A | |
| L15-6000 | Tape/Finish GWB | 4 | 0 | 12-Sep-14 A | 20-Sep-14 A | |
| L17-6016 | Electrical RI | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-6028 | PreRock at Heat Pumps | 2 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L17-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L17-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |

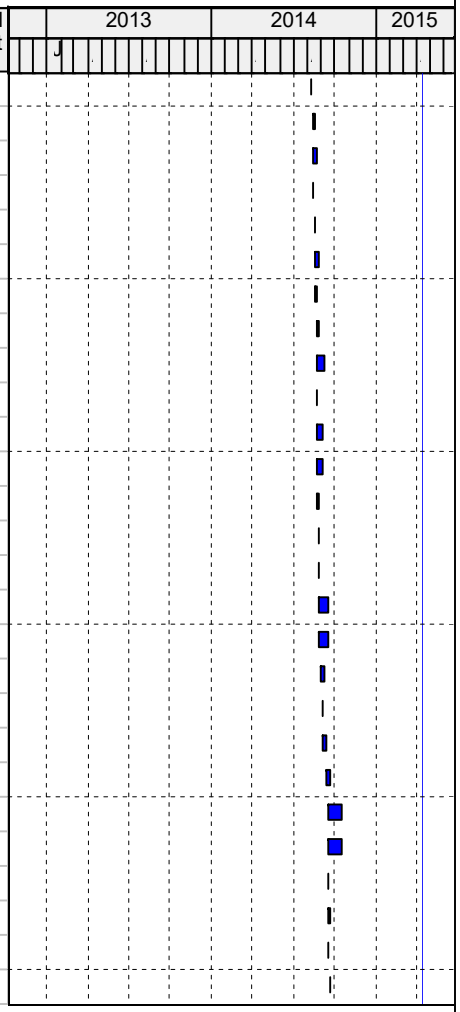


Actual Work | Critical Remai...
Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L17-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 24-Sep-14 A | 27-Sep-14 A | |
| L17-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L16-6024 | Inspections for GWB Cover | 1 | 0 | 08-Oct-14 A | 09-Oct-14 A | |
| L16-6000 | Tape/Finish GWB | 4 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6024 | Inspections for GWB Cover | 1 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6000 | Tape/Finish GWB | 6 | 0 | 30-Oct-14 A | 07-Nov-14 A | |
| **Mechanical Penthouse** | | | | | | |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 0 | 11-Jun-14 A | 20-Jun-14 A | |
| PH-6006 | PH - Exterior Wall Framing (including PH roof parapet | 6 | 0 | 12-Jun-14 A | 14-Jul-14 A | |
| PH-6014 | PH - Plumbing/Piping RI | 40 | 0 | 25-Jun-14 A | 05-Nov-14 A | |
| PH-6002 | PH - Layout | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| PH-6008 | PH - Interior Wall Framing | 3 | 0 | 24-Jul-14 A | 08-Aug-14 A | |
| PH-6020 | PH - H Mtl Frames | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| PH-6012 | PH - Fire Sprinkler RI | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |
| PH-6018 | PH - HVAC RI | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |
| PH-6016 | PH - Electrical RI | 10 | 0 | 23-Sep-14 A | 14-Nov-14 A | |
| PH-6022 | PH - Fire Alarm / Elec Specialties RI | 10 | 0 | 23-Sep-14 A | 14-Nov-14 A | |
| **Finishes** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL4-8100 | LL4 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| LL4-8102 | LL4 - GWB Hang (incl. screw inspection) | 3 | 0 | 27-Oct-14 A | 10-Dec-14 A | |
| LL4-8114 | LL4 - Striping / Signage (DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL4-8104 | LL4 - Int Painting | 3 | 0 | 22-Dec-14 A | 24-Dec-14 A | |

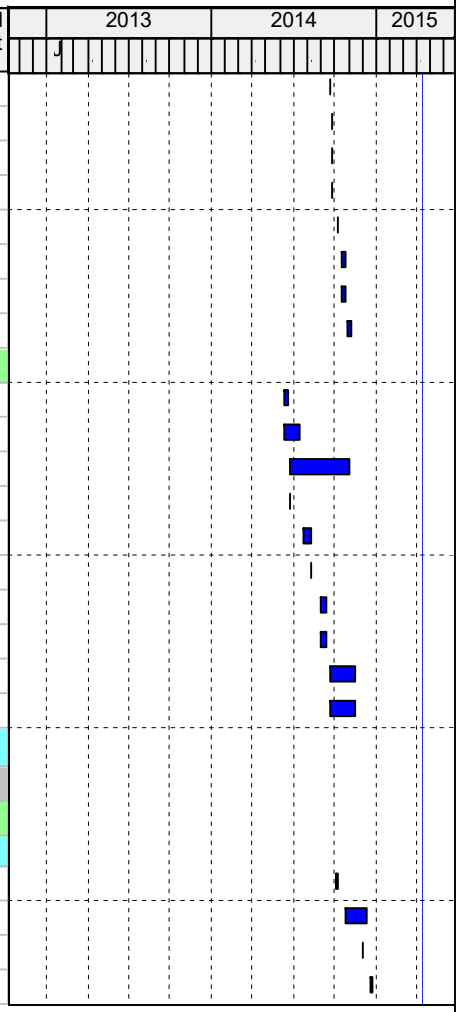



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8122 | LL4 - Plumbing Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL4-8108 | Electrical trim & finish | 5 | 0 | 29-Dec-14 A | 16-Feb-15 A | |
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL4-8126 | Install doors & hardware | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL4-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 22-Jan-15 A | 26-Jan-15 A | |
| LL4-8124 | Flooring - VCT | 4 | 0 | 05-Feb-15 A | 06-Feb-15 A | |
| LL4-8110 | HVAC trim | 2 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| LL4-8134 | Final Cleaning | 2 | 2 | 04-May-15 | 05-May-15 | 10 |
| LL4-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 06-May-15 | 08-May-15 | 10 |
| LL4-8214 | LL4 Floor Complete | 0 | 0 | | 08-May-15 | 10 |
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL3-8100 | LL3 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| LL3-8102 | LL3 - GWB Hang (incl. screw inspection) | 3 | 0 | 27-Oct-14 A | 10-Dec-14 A | |
| LL3-8114 | LL3 - Striping / Signage [DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL3-8104 | LL3 - Int Painting | 3 | 0 | 22-Dec-14 A | 24-Dec-14 A | |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL3-8108 | Electrical trim & finish | 5 | 0 | 29-Dec-14 A | 16-Feb-15 A | |
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL3-8126 | Install doors & hardware | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL3-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 22-Jan-15 A | 03-Feb-15 A | |
| LL3-8124 | Flooring - VCT | 4 | 0 | 06-Feb-15 A | 07-Feb-15 A | |
| LL3-8110 | HVAC trim | 2 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| LL3-8134 | Final Cleaning | 2 | 2 | 04-May-15 | 05-May-15 | 10 |
| LL3-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 06-May-15 | 08-May-15 | 10 |
| LL3-8214 | LL3 Floor Complete | 0 | 0 | | 08-May-15 | 10 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |

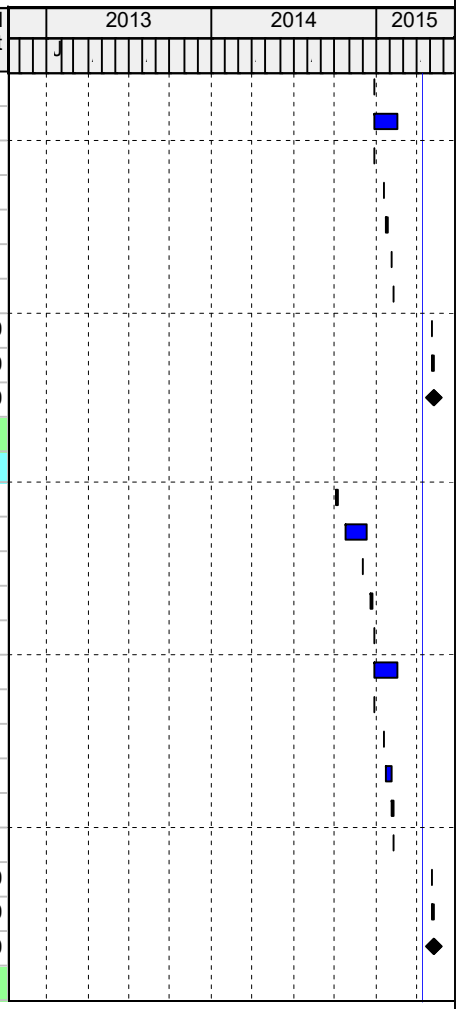



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Corridors / Common / Public Areas** | | | | | | |
| LL2E-8102 | LL2 - GWB Hang / Tape / Finish @ Electrical Rooms | 8 | 0 | 24-Jun-14 A | 03-Jul-14 A | |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish & Inspection | 6 | 0 | 16-Sep-14 A | 22-Dec-14 A | |
| LL2-8100 | LL2 - Insulation | 5 | 0 | 16-Sep-14 A | 09-Oct-14 A | |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 5 | 0 | 17-Sep-14 A | 27-Oct-14 A | |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| LL2-8104 | LL2 - Int Painting | 5 | 0 | 25-Nov-14 A | 23-Dec-14 A | |
| LL2-8114 | LL2 - Striping / Signage [DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL2-8116 | LL2 - Finish Carpentry / Millwork [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL2-8124 | Flooring - VCT | 4 | 0 | 06-Feb-15 A | 10-Mar-15 A | |
| LL2-8126 | Install doors & hardware | 3 | 0 | 09-Feb-15 A | 16-Feb-15 A | |
| LL2-8122 | Complete MEP trim | 2 | 2 | 27-Apr-15 | 28-Apr-15 | 8 |
| LL2-8136 | Chainlink Fencing / Gate @ Recycling at Garage | 5 | 5 | 27-Apr-15 | 01-May-15 | 5 |
| LL2-8120 | Install bollards at Garage | 5 | 5 | 27-Apr-15 | 01-May-15 | 5 |
| LL2-8128 | Entry Gates at Garage | 3 | 3 | 30-Apr-15 | 04-May-15 | 4 |
| LL2-8134 | Final Cleaning | 2 | 2 | 12-May-15 | 13-May-15 | 4 |
| LL2-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 14-May-15 | 18-May-15 | 4 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 31-Jul-14 A | |
| LL1-Z2U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 09-May-14 A | |
| LL1-Z3U-8102 | Above Ceiling GWB (At All Areas North of Q-Line) | 5 | 0 | 10-Feb-14 A | 20-Jun-14 A | |
| L1BU-8102 | Above Ceiling GWB [including East Service Corridor] | 5 | 0 | 06-Jun-14 A | 11-Jun-14 A | |
| L1LU-8102 | Above Ceiling GWB | 5 | 0 | 24-Jun-14 A | 13-Oct-14 A | |
| L1KU-8102 | Above Ceiling GWB | 2 | 0 | 26-Jun-14 A | 22-Aug-14 A | |
| LL1-8100 | Insulation | 5 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| LL1-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 28-Jul-14 A | 06-Aug-14 A | |

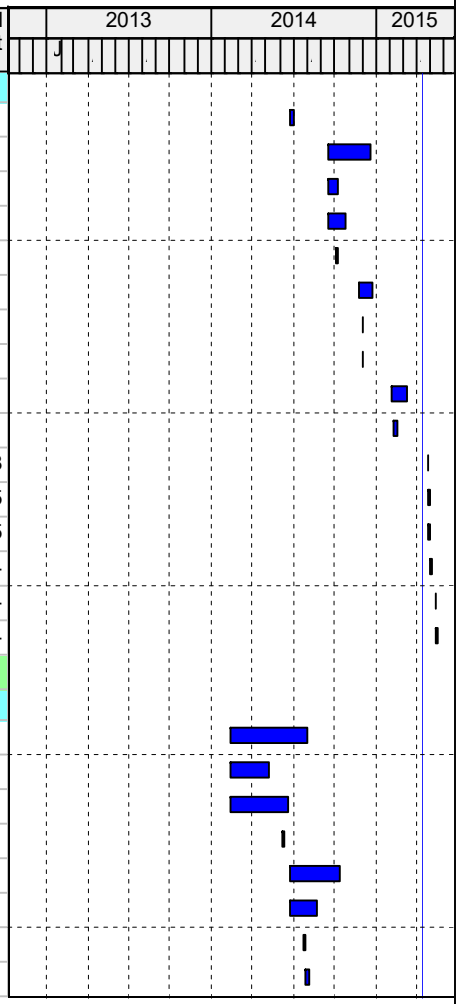



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-8102 | GWB Hang (Walls) & Inspection | 4 | 0 | 11-Aug-14 A | 14-Aug-14 A | |
| LL1-Z2-8100 | Insulation | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| LL1-8215 | GWB Tape (Walls) | 10 | 0 | 16-Aug-14 A | 07-Nov-14 A | |
| LL1-Z3-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 15-Sep-14 A | 07-Oct-14 A | |
| LL1-Z3-8100 | Insulation | 5 | 0 | 15-Sep-14 A | 24-Sep-14 A | |
| LL1-Z2-8215 | GWB Tape (Walls/Ceilings) | 7 | 0 | 29-Sep-14 A | 07-Nov-14 A | |
| L1B-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L1K-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| LL1-Z3-8215 | GWB Tape (Walls & Ceilings) | 7 | 0 | 07-Oct-14 A | 18-Nov-14 A | |
| L1K-8102 | GWB Hang (Walls) & Inspection | 8 | 0 | 09-Oct-14 A | 31-Oct-14 A | |
| L1L-8100 | Insulation | 4 | 0 | 13-Oct-14 A | 16-Oct-14 A | |
| L1B-8102 | GWB Hang (Walls) & Inspection - Main Ballroom N/S/ | 4 | 0 | 16-Oct-14 A | 22-Oct-14 A | |
| L1L-8102 | GWB hang walls (Dining & Lounge) | 4 | 0 | 30-Oct-14 A | 05-Feb-15 A | |
| L1K-8215 | GWB Tape (Walls & Ceilings) | 4 | 0 | 05-Nov-14 A | 18-Nov-14 A | |
| LL1-Z3-8104 | Prime Paint | 4 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| LL1-8104 | Prime Paint & First Coat Finish Paint | 5 | 0 | 02-Dec-14 A | 12-Dec-14 A | |
| L1K-8106 | Wall coverings - FRP | 8 | 0 | 19-Dec-14 A | 08-Jan-15 A | |
| LL1-Z3-8114 | Ceiling grid & inspection | 4 | 0 | 13-Jan-15 A | 16-Jan-15 A | |
| LL1-8126 | Install doors & hardware | 5 | 0 | 26-Jan-15 A | 03-Feb-15 A | |
| L1L-8215 | GWB hang ceilings (Dining & Lounge) | 5 | 0 | 29-Jan-15 A | 05-Feb-15 A | |
| LL1-8116 | Finish carpentry/millwork | 10 | 0 | 05-Feb-15 A | 02-Mar-15 A | |
| L1K-8114 | Ceiling grid & inspection (east end) | 8 | 0 | 05-Feb-15 A | 13-Mar-15 A | |
| LL1-Z3-8126 | Install doors & hardware | 5 | 0 | 09-Feb-15 A | 12-Feb-15 A | |
| L1K-8124 | Flooring - VCT | 3 | 1 | 10-Feb-15 A | 05-May-15 | 1 |
| LL1-8114 | Ceiling grid & inspection | 4 | 0 | 11-Feb-15 A | 20-Feb-15 A | |
| LL1-8118 | Lighting & electrical drops to grid | 3 | 0 | 12-Feb-15 A | 20-Feb-15 A | |
| LL1-Z2-8104 | Paint, prime at Jr. Ballrooms | 2 | 0 | 12-Feb-15 A | 13-Feb-15 A | |

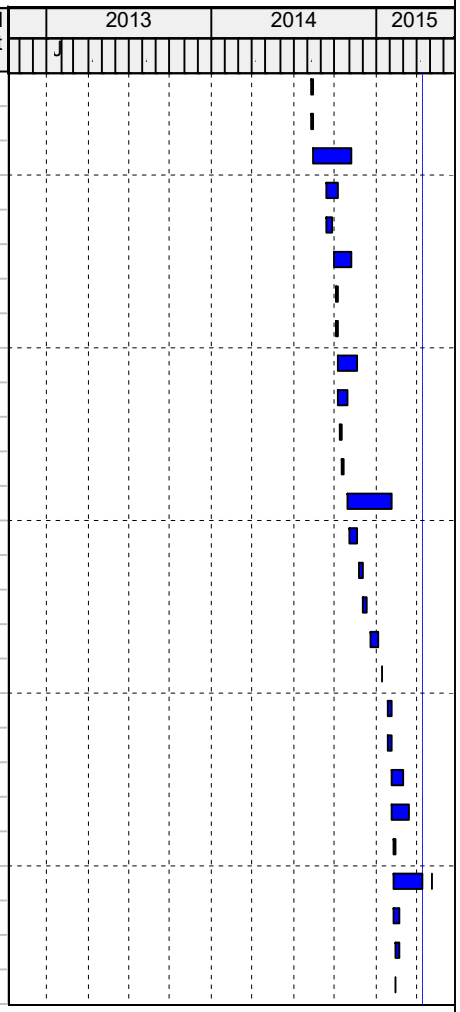



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8104 | Paint, prime | 2 | 0 | 13-Feb-15 A | 17-Feb-15 A | |
| LL1-Z2-8126 | Install doors & hardware | 3 | 0 | 16-Feb-15 A | 06-Apr-15 A | |
| LL1-8112 | Fire sprinkler drops to grid | 2 | 0 | 17-Feb-15 A | 20-Feb-15 A | |
| LL1-Z2-8106 | Wall coverings - vinyl at Jr. Ballrooms | 2 | 0 | 18-Feb-15 A | 19-Feb-15 A | |
| LL1-Z2-8114 | Ceiling grid & inspection | 5 | 0 | 18-Feb-15 A | 26-Feb-15 A | |
| L1L-8114 | Install 9-wood ceiling supports - north of Grid K | 3 | 0 | 19-Feb-15 A | 26-Feb-15 A | |
| LL1-Z2-8116 | Finish carpentry/millwork | 10 | 0 | 20-Feb-15 A | 02-Mar-15 A | |
| L1K-8104 | Paint, prime | 2 | 0 | 26-Feb-15 A | 27-Feb-15 A | |
| L1B-8104 | Paint, prime & first coat finish | 3 | 0 | 06-Mar-15 A | 10-Mar-15 A | |
| LL1-Z2-8124 | Flooring - VCT at service corridor | 2 | 0 | 09-Mar-15 A | 11-Mar-15 A | |
| LL1-Z3-8124 | Flooring - epoxy at Food Prep (including prep) | 6 | 0 | 09-Mar-15 A | 13-Mar-15 A | |
| LL1-Z2-8112 | Fire sprinkler drops to grid | 2 | 0 | 16-Mar-15 A | 31-Mar-15 A | |
| LL1-Z2-8118 | Lighting & electrical drops to grid | 3 | 0 | 16-Mar-15 A | 30-Mar-15 A | |
| LL1-Z3-8118 | Lighting & electrical drops at ceiling | 3 | 0 | 16-Mar-15 A | 18-Mar-15 A | |
| LL1-Z3-8112 | Fire sprinkler drops/trim at ceiling | 2 | 1 | 17-Mar-15 A | 13-Apr-15 | 15 |
| L1L-8140 | Install 9-wood ceiling - north of Grid K | 4 | 0 | 19-Mar-15 A | 31-Mar-15 A | |
| L1L-8116 | Finish carpentry/millwork - north of Grid K | 5 | 0 | 23-Mar-15 A | 27-Mar-15 A | |
| L1L-8126 | Install doors & hardware | 2 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| LL1-8124 | Flooring - VCT at storage areas, janitorial, mechanica | 3 | 0 | 25-Mar-15 A | 26-Mar-15 A | |
| L1B-8126 | Install doors & hardware at Ballrooms | 2 | 1 | 25-Mar-15 A | 13-Apr-15 | 10 |
| L1L-8112 | Fire sprinkler trim - north of Grid K | 1 | 0 | 31-Mar-15 A | 31-Mar-15 A | |
| L1K-8116 | Finish carpentry/millwork | 2 | 0 | 06-Apr-15 A | 06-Apr-15 A | |
| L1K-8126 | Install doors & hardware | 3 | 0 | 07-Apr-15 A | 08-Apr-15 A | |
| L1K-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8106 | Wall coverings - vinyl | 5 | 3 | 09-Apr-15 A | 15-Apr-15 | 14 |
| LL1-Z3-8116 | Install VCT base | 3 | 3 | 13-Apr-15 | 15-Apr-15 | 15 |
| L1B-8116 | Finish carpentry/millwork at Ballrooms | 5 | 5 | 13-Apr-15 | 17-Apr-15 | 8 |

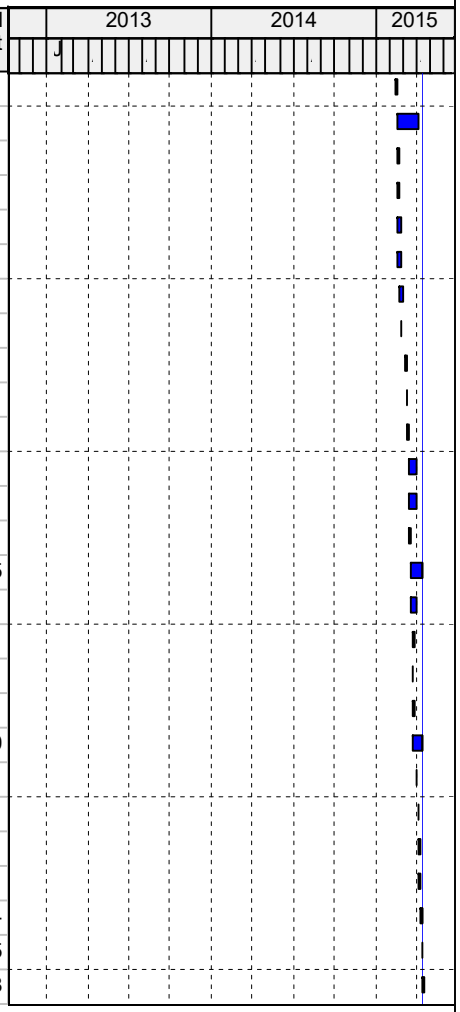



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-8114 | Ceiling grid & inspection | 3 | 3 | 13-Apr-15 | 15-Apr-15 | 7 |
| L1L-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 1 | 13-Apr-15 | 13-Apr-15 | 11 |
| LL1-Z3-8140 | Complete acoustical ceiling tile | 2 | 2 | 14-Apr-15 | 15-Apr-15 | 15 |
| L1K-8112 | Fire sprinkler trim | 1 | 1 | 14-Apr-15 | 14-Apr-15 | 18 |
| LL1-Z2-8140 | Complete acoustical ceiling tile | 2 | 2 | 15-Apr-15 | 16-Apr-15 | 14 |
| L1L-8124 | Flooring - wood - north of Grid K | 4 | 4 | 20-Apr-15 | 23-Apr-15 | 7 |
| LL1-Z3-8134 | Final Cleaning | 2 | 2 | 23-Apr-15 | 24-Apr-15 | 17 |
| LL1-Z3-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 27-Apr-15 | 29-Apr-15 | 17 |
| L1B-8124 | Flooring - carpet at Ballrooms | 5 | 5 | 27-Apr-15 | 01-May-15 | 3 |
| L1B-8164 | Ceiling grid & inspection at Prefunction 2 | 2 | 2 | 30-Apr-15 | 01-May-15 | 0 |
| L1B-8140 | Complete acoustical ceiling tile | 2 | 2 | 04-May-15 | 05-May-15 | 3 |
| LL1-Z2-8134 | Final Cleaning | 2 | 2 | 05-May-15 | 06-May-15 | 9 |
| LL1-8134 | Final Cleaning | 2 | 2 | 07-May-15 | 08-May-15 | 7 |
| LL1-Z2-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 07-May-15 | 11-May-15 | 9 |
| LL1-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 11-May-15 | 13-May-15 | 7 |
| L1L-8134 | Final Cleaning | 2 | 2 | 13-May-15 | 14-May-15 | 3 |
| L1K-8134 | Final Cleaning | 2 | 2 | 13-May-15 | 14-May-15 | 3 |
| L1L-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 15-May-15 | 19-May-15 | 3 |
| L1K-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 15-May-15 | 19-May-15 | 3 |
| L1B-8134 | Final Cleaning | 2 | 2 | 18-May-15 | 19-May-15 | 0 |
| L1B-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 20-May-15 | 22-May-15 | 0 |
| **Corridors / Common / Public Areas** | | | | | | |
| LL1-8200 | Wall coverings - vinyl | 4 | 0 | 17-Dec-14 A | 19-Jan-15 A | |
| LL1-Z3-8200 | Paint, first coat finish | 4 | 0 | 07-Jan-15 A | 12-Jan-15 A | |
| LL1-Z3-8204 | HVAC drops/trim at ceiling | 2 | 0 | 02-Feb-15 A | 17-Mar-15 A | |
| LL1-8204 | HVAC drops/trim to grid | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| LL1-Z2-8200 | Paint, first coat finish at Jr. Ballrooms | 1 | 0 | 16-Feb-15 A | 16-Feb-15 A | |

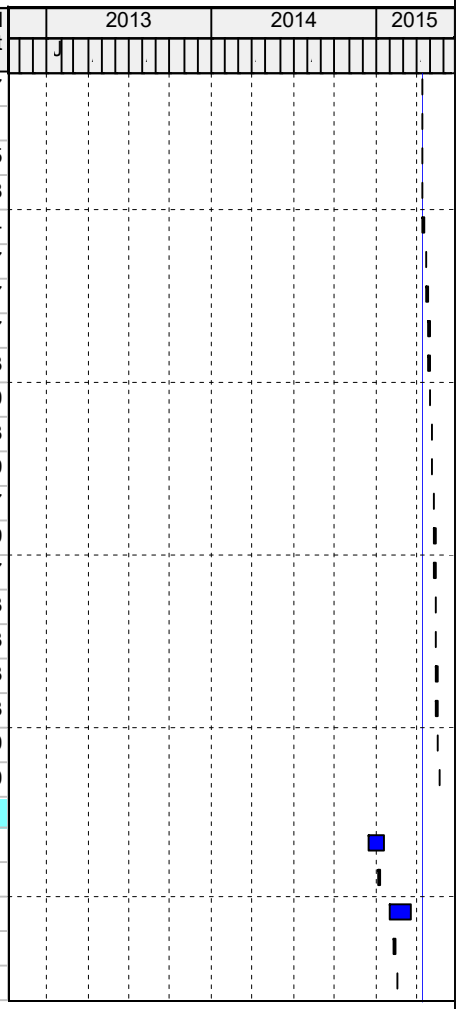


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8200 | Paint, first coat finish | 2 | 0 | 18-Feb-15 A | 18-Feb-15 A | |
| L1K-8200 | Paint, first coat finish | 1 | 0 | 02-Mar-15 A | 02-Mar-15 A | |
| LL1-Z2-8204 | HVAC drops/trim to grid | 2 | 0 | 16-Mar-15 A | 17-Mar-15 A | |
| L1L-8204 | HVAC trim at ceiling - north of Grid K | 1 | 1 | 27-Mar-15 A | 13-Apr-15 | 10 |
| L1B-8200 | Paint ceiling clouds | 3 | 0 | 02-Apr-15 A | 03-Apr-15 A | |
| L1K-8204 | HVAC drops/trim at ceiling | 1 | 1 | 14-Apr-15 | 14-Apr-15 | 8 |
| LL1-Z3-8214 | LL1, Zone 3 Complete | 0 | 0 | | 29-Apr-15 | 17 |
| L1B-8201 | Complete paint final coat & touch-up | 2 | 2 | 04-May-15 | 05-May-15 | 3 |
| LL1-Z2-8214 | LL1 Zone 2 Complete | 0 | 0 | | 11-May-15 | 9 |
| LL1-8214 | LL1, Zone 1 Complete | 0 | 0 | | 13-May-15 | 7 |
| L1L-8214 | L1, Zone 4 Complete | 0 | 0 | | 19-May-15 | 3 |
| L1K-8214 | L1, Zone 1 Complete | 0 | 0 | | 19-May-15 | 3 |
| L1B-8214 | L1, Zone 2 Complete | 0 | 0 | | 22-May-15 | 0 |
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8100 | L2 - Insulation - North Half | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L02-8102 | L2 - GWB Hang / Tape / Finish - North Half | 7 | 0 | 23-Oct-14 A | 17-Dec-14 A | |
| L02-8126 | Install doors & hardware at south half | 5 | 2 | 23-Mar-15 A | 16-Apr-15 | 3 |
| L02-8112 | Fire sprinkler drops/trim at south half | 2 | 1 | 01-Apr-15 A | 17-Apr-15 | 13 |
| L02-8120 | Ceramic tile | 15 | 8 | 02-Apr-15 A | 22-Apr-15 | 3 |
| L02-8104 | Paint, prime & first coat finish at north half | 2 | 0 | 03-Apr-15 A | 09-Apr-15 A | |
| L02-8106 | Wall coverings - vinyl at south half | 4 | 2 | 07-Apr-15 A | 14-Apr-15 | 3 |
| L02-8110 | HVAC drops/trim at south half | 2 | 2 | 13-Apr-15 | 14-Apr-15 | 1 |
| L02-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 15-Apr-15 | 16-Apr-15 | 1 |
| L02-8124 | Flooring - carpet | 4 | 4 | 20-Apr-15 | 23-Apr-15 | 7 |
| L02-8122 | Plumbing fixtures & trim | 4 | 4 | 23-Apr-15 | 28-Apr-15 | 3 |
| L02-8116 | Finish carpentry/millwork at south half | 2 | 2 | 24-Apr-15 | 27-Apr-15 | 7 |

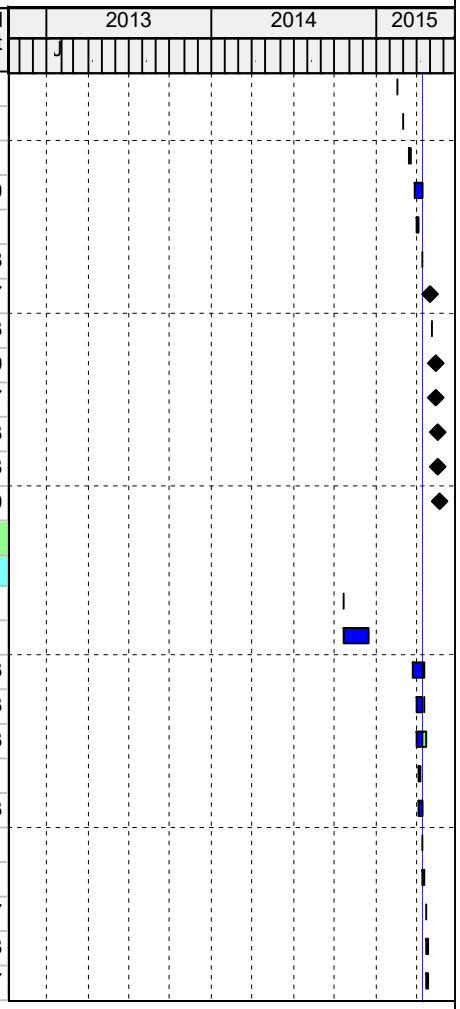



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8128 | Install bathroom accessories | 3 | 3 | 29-Apr-15 | 01-May-15 | 3 |
| L02-8136 | Lockers / Benches @ Locker Rooms | 3 | 3 | 29-Apr-15 | 01-May-15 | 3 |
| L02-8108 | Complete MEP trim | 2 | 2 | 04-May-15 | 05-May-15 | 3 |
| L02-8134 | Final Cleaning | 2 | 2 | 13-May-15 | 14-May-15 | 3 |
| L02-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 15-May-15 | 19-May-15 | 3 |
| **Corridors** | | | | | | |
| L02-8200 | Complete paint final coat & touch-up | 2 | 2 | 04-May-15 | 05-May-15 | 3 |
| L02-8214 | Floor Complete | 0 | 0 | | 19-May-15 | 3 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L03-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L04-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L05-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L06-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L07-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L08-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L09-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L10-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L11-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L12-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L14-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L15-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L16-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L17-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L03-8102S | Stock GWB | 2 | 0 | 27-Jun-14 A | 08-Jul-14 A | |
| L04-8102 | Hang GWB & Inspection | 4 | 0 | 07-Jul-14 A | 16-Jul-14 A | |

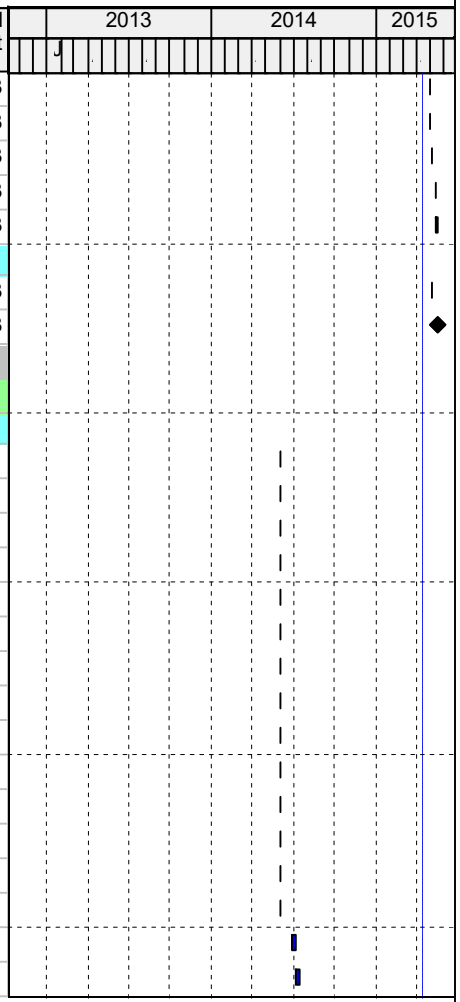



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8102S | Stock GWB | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-8102 | Hang GWB & Inspection | 5 | 0 | 09-Jul-14 A | 22-Jul-14 A | |
| L05-8102S | Stock GWB | 2 | 0 | 10-Jul-14 A | 14-Jul-14 A | |
| L05-8102 | Hang GWB & Inspection | 4 | 0 | 17-Jul-14 A | 23-Jul-14 A | |
| L06-8102S | Stock GWB | 2 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L04-8104 | Paint (Prime) | 2 | 0 | 28-Jul-14 A | 05-Aug-14 A | |
| L03-8104 | Paint (Prime) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L03-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L07-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L08-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L06-8102 | Hang GWB & Inspection | 5 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L07-8102 | Hang GWB & Inspection | 6 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L04-8105 | Paint (First Coat & Ceilings) | 5 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L05-8104 | Paint (Prime) | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| L09-8102S | Stock GWB | 2 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 07-Aug-14 A | 11-Aug-14 A | |
| L09-8102 | Hang GWB & Inspection | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| L08-8102 | Hang GWB & Inspection | 6 | 0 | 11-Aug-14 A | 15-Aug-14 A | |
| L06-8104 | Paint (Prime) | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L10-8102S | Stock GWB | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-8102 | Hang GWB & Inspection | 4 | 0 | 13-Aug-14 A | 18-Aug-14 A | |
| L06-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 14-Aug-14 A | 18-Aug-14 A | |
| L11-8102S | Stock GWB | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L07-8104 | Paint (Prime) | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L11-8102 | Hang GWB & Inspection | 4 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| L07-8105 | Paint (First Coat & Ceilings) | 4 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L09-8104 | Paint (Prime) | 2 | 0 | 20-Aug-14 A | 28-Aug-14 A | |

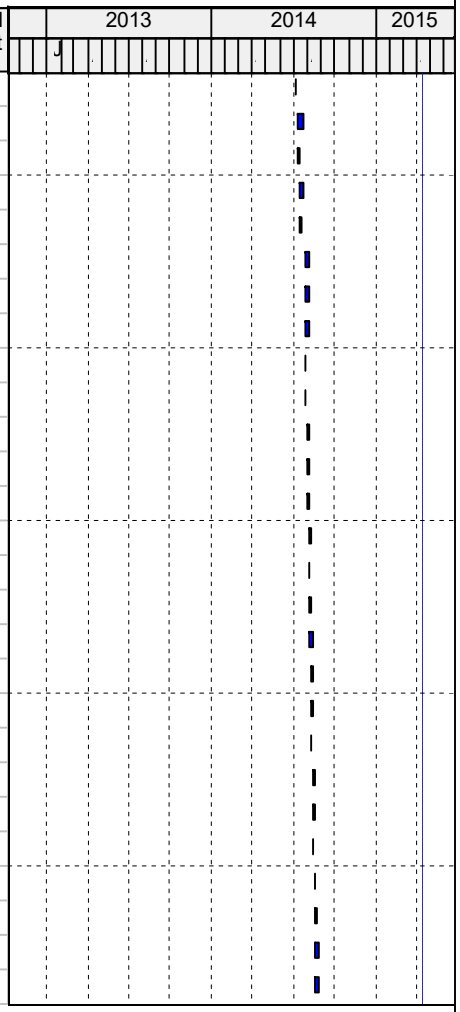



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8104 | Paint (Prime) | 2 | 0 | 22-Aug-14 A | 25-Aug-14 A | |
| L12-8102 | Hang GWB & Inspection | 4 | 0 | 22-Aug-14 A | 30-Aug-14 A | |
| L12-8102S | Stock GWB | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8108 | Elec Trim / Finish | 4 | 0 | 25-Aug-14 A | 04-Sep-14 A | |
| L08-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L03-8118 | Fire Alarm Trim / Finish | 3 | 0 | 27-Aug-14 A | 29-Sep-14 A | |
| L14-8102S | Stock GWB | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L09-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 29-Aug-14 A | 09-Sep-14 A | |
| L14-8102 | Hang GWB & Inspection | 5 | 0 | 29-Aug-14 A | 05-Sep-14 A | |
| L03-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 02-Sep-14 A | 05-Sep-14 A | |
| L04-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 04-Sep-14 A | 09-Sep-14 A | |
| L10-8104 | Paint (Prime) | 2 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| L15-8102S | Stock GWB | 1 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L15-8102 | Hang GWB & Inspection | 5 | 0 | 06-Sep-14 A | 12-Sep-14 A | |
| L03-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8108 | Elec Trim / Finish | 4 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L04-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 11-Sep-14 A | |
| L05-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 08-Sep-14 A | 12-Sep-14 A | |
| L10-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 08-Sep-14 A | 12-Sep-14 A | |
| L11-8104 | Paint (Prime) | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L04-8116 | Install Base at Guestrooms | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L11-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 10-Sep-14 A | 22-Sep-14 A | |
| L03-8116 | Install Base at Guestrooms | 5 | 0 | 12-Sep-14 A | 16-Sep-14 A | |
| L12-8104 | Paint (Prime) | 2 | 0 | 12-Sep-14 A | 17-Sep-14 A | |
| L05-8116 | Install Base at Guestrooms | 5 | 0 | 16-Sep-14 A | 24-Sep-14 A | |
| L06-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 16-Sep-14 A | 22-Sep-14 A | |

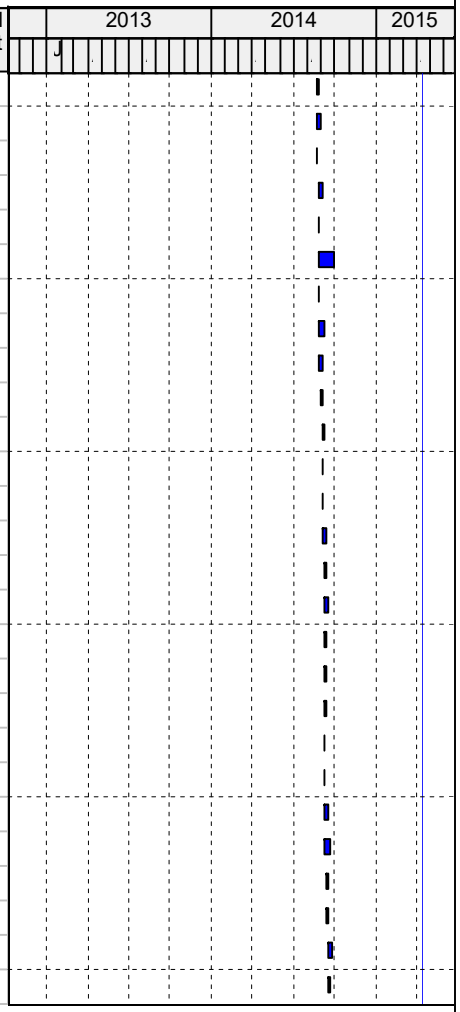



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8108 | Elec Trim / Finish | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L07-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 17-Sep-14 A | 23-Sep-14 A | |
| L12-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 17-Sep-14 A | 06-Oct-14 A | |
| L06-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L07-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L14-8104 | Paint (Prime) | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L06-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L06-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L08-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L14-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 24-Sep-14 A | 06-Oct-14 A | |
| L15-8104 | Paint (Prime) | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L03-8110 | HVAC Grilles & Registers | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L03-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8118 | Fire Alarm Trim / Finish | 3 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L10-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L08-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 30-Sep-14 A | 06-Oct-14 A | |
| L03-8126 | Install Doors | 3 | 0 | 01-Oct-14 A | 07-Oct-14 A | |
| L03-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 01-Oct-14 A | 28-Oct-14 A | |
| L04-8126 | Install Doors | 3 | 0 | 02-Oct-14 A | 09-Oct-14 A | |
| L08-8116 | Install Base at Guestrooms | 5 | 0 | 02-Oct-14 A | 08-Oct-14 A | |
| L04-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8118 | Fire Alarm Trim / Finish | 3 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8108 | Elec Trim / Finish | 4 | 0 | 06-Oct-14 A | 08-Oct-14 A | |

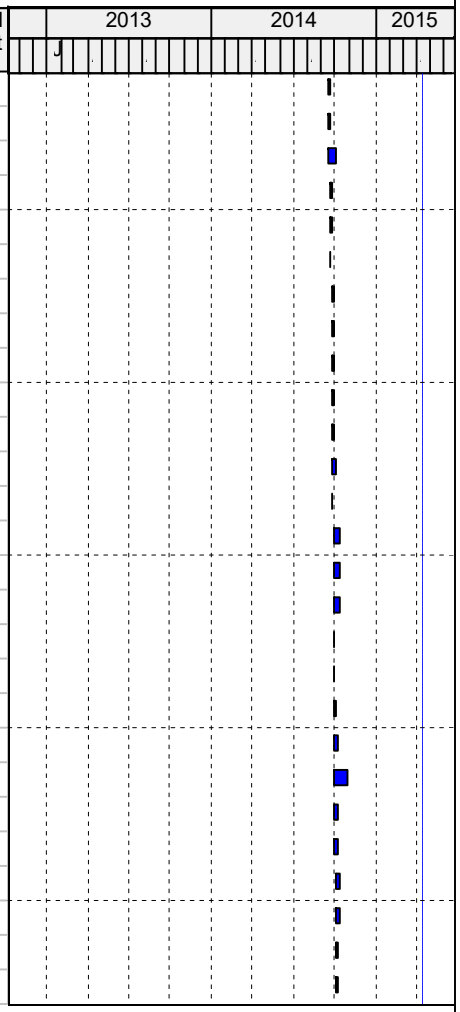



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8105 | Paint - First Coast & Ceilings | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8126 | Install Doors | 3 | 0 | 08-Oct-14 A | 10-Oct-14 A | |
| L09-8116 | Install Base and Door Thresholds | 5 | 0 | 08-Oct-14 A | 15-Oct-14 A | |
| L09-8124 | Install Flooring | 5 | 0 | 08-Oct-14 A | 14-Oct-14 A | |
| L16-8102S | Stock GWB | 1 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L09-8112 | Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 10-Oct-14 A | |
| L16-8102 | Hang GWB & Inspection | 4 | 0 | 10-Oct-14 A | 17-Oct-14 A | |
| L06-8118 | Fire Alarm Trim / Finish | 3 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L09-8108 | Lighting and Electrical Trim | 3 | 0 | 13-Oct-14 A | 15-Oct-14 A | |
| L10-8124 | Install Flooring | 5 | 0 | 13-Oct-14 A | 16-Oct-14 A | |
| L11-8112 | Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L03-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 14-Oct-14 A | 04-Nov-14 A | |
| L06-8110 | HVAC Grilles & Registers | 2 | 0 | 14-Oct-14 A | 21-Oct-14 A | |
| L06-8126 | Install Doors | 2 | 0 | 14-Oct-14 A | 20-Oct-14 A | |
| L07-8118 | Fire Alarm Trim / Finish | 3 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L12-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L14-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L08-8118 | Fire Alarm Trim / Finish | 3 | 0 | 15-Oct-14 A | 16-Oct-14 A | |
| L10-8116 | Install Base and Door Thresholds | 5 | 0 | 15-Oct-14 A | 23-Oct-14 A | |
| L15-8112 | Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 16-Oct-14 A | |
| L04-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 16-Oct-14 A | 11-Nov-14 A | |
| L11-8124 | Install Flooring | 5 | 0 | 16-Oct-14 A | 22-Oct-14 A | |
| L17-8102S | Stock GWB | 1 | 0 | 17-Oct-14 A | 17-Oct-14 A | |
| L07-8126 | Install Doors | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |
| L09-8118 | Fire Alarm Trim | 2 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| L05-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 21-Oct-14 A | 14-Nov-14 A | |
| L08-8126 | Install Doors | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |

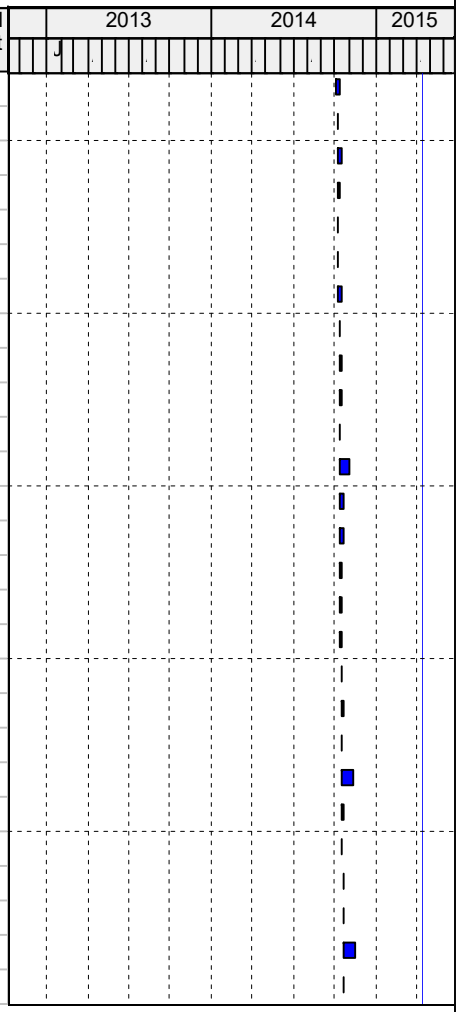



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8118 | Fire Alarm Trim | 2 | 0 | 21-Oct-14 A | 21-Oct-14 A | |
| L09-8126 | Install Doors | 2 | 0 | 22-Oct-14 A | 23-Oct-14 A | |
| L11-8118 | Fire Alarm Trim | 2 | 0 | 22-Oct-14 A | 22-Oct-14 A | |
| L06-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 23-Oct-14 A | 19-Nov-14 A | |
| L10-8126 | Install Doors | 2 | 0 | 23-Oct-14 A | 27-Oct-14 A | |
| L12-8124 | Install Flooring | 5 | 0 | 23-Oct-14 A | 29-Oct-14 A | |
| L12-8118 | Fire Alarm Trim | 2 | 0 | 23-Oct-14 A | 23-Oct-14 A | |
| L11-8116 | Install Base and Door Thresholds | 5 | 0 | 24-Oct-14 A | 26-Nov-14 A | |
| L07-8110 | HVAC Grilles & Registers | 2 | 0 | 27-Oct-14 A | 28-Oct-14 A | |
| L10-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |
| L11-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |
| L17-8102 | Hang GWB & Inspection | 4 | 0 | 27-Oct-14 A | 03-Nov-14 A | |
| L07-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 28-Oct-14 A | 26-Nov-14 A | |
| L08-8120 | Bathrooms - Install Countertops | 3 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L11-8126 | Install Doors | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L12-8108 | Lighting and Electrical Trim | 3 | 0 | 28-Oct-14 A | 30-Oct-14 A | |
| L12-8116 | Install Base and Door Thresholds | 5 | 0 | 28-Oct-14 A | 03-Dec-14 A | |
| L14-8118 | Fire Alarm Trim | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L05-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Oct-14 A | 31-Oct-14 A | |
| L06-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Oct-14 A | 31-Oct-14 A | |
| L12-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L14-8108 | Lighting and Electrical Trim | 3 | 0 | 29-Oct-14 A | 03-Nov-14 A | |
| L14-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8118 | Fire Alarm Trim | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L04-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 30-Oct-14 A | 04-Nov-14 A | |
| L07-8120 | Bathrooms - Install Countertops | 3 | 0 | 03-Nov-14 A | 05-Nov-14 A | |

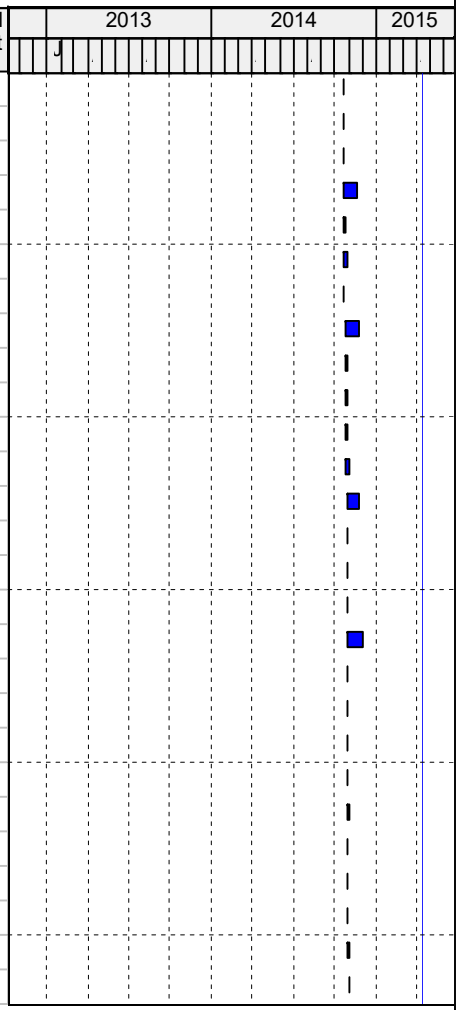



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8110 | HVAC Grilles & Registers | 2 | 0 | 03-Nov-14 A | 04-Nov-14 A | |
| L09-8120 | Bathrooms - Install Countertops | 3 | 0 | 03-Nov-14 A | 05-Nov-14 A | |
| L10-8120 | Bathrooms - Install Countertops | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| L15-8108 | Lighting and Electrical Trim | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| L11-8120 | Bathrooms - Install Countertops | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| L16-8104 | Paint - Prime | 2 | 0 | 05-Nov-14 A | 06-Nov-14 A | |
| L05-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 07-Nov-14 A | 12-Nov-14 A | |
| L16-8105 | Paint - First Coat & Ceilings | 3 | 0 | 07-Nov-14 A | 11-Nov-14 A | |
| L12-8120 | Bathrooms - Install Countertops | 3 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L14-8124 | Install Flooring | 5 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L06-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 13-Nov-14 A | 17-Nov-14 A | |
| L15-8124 | Install Flooring | 5 | 0 | 17-Nov-14 A | 25-Nov-14 A | |
| L17-8104 | Paint - Prime | 2 | 0 | 17-Nov-14 A | 18-Nov-14 A | |
| L14-8116 | Install Base and Door Thresholds | 5 | 0 | 18-Nov-14 A | 08-Dec-14 A | |
| L16-8126 | Install Doors | 2 | 0 | 18-Nov-14 A | 19-Nov-14 A | |
| L07-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 19-Nov-14 A | 25-Nov-14 A | |
| L15-8116 | Install Base and Door Thresholds | 5 | 0 | 20-Nov-14 A | 08-Dec-14 A | |
| L03-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L04-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L05-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L08-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| L17-8105 | Paint - First Coat & Ceilings | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L16-8124 | Install Flooring | 5 | 0 | 25-Nov-14 A | 03-Dec-14 A | |
| L16-8112 | Fire Sprinkler Trim | 2 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| L16-8118 | Fire Alarm Trim | 2 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| L06-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L07-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |

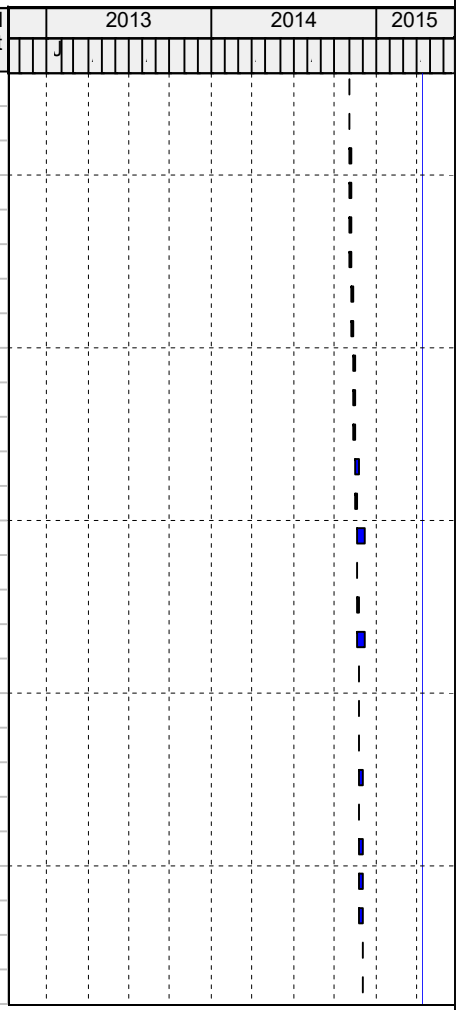



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 01-Dec-14 A | 08-Dec-14 A | |
| L08-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L09-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 01-Dec-14 A | 10-Dec-14 A | |
| L16-8108 | Lighting and Electrical Trim | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L17-8126 | Install Doors | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| L16-8116 | Install Base and Door Thresholds | 5 | 0 | 02-Dec-14 A | 15-Dec-14 A | |
| L17-8112 | Fire Sprinkler Trim | 2 | 0 | 02-Dec-14 A | 02-Dec-14 A | |
| L09-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 03-Dec-14 A | 08-Dec-14 A | |
| L09-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L10-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L11-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L17-8118 | Fire Alarm Trim | 2 | 0 | 03-Dec-14 A | 03-Dec-14 A | |
| L12-8107 | Paint Final Coat | 3 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L14-8120 | Bathrooms - Install Countertops | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L17-8108 | Lighting and Electrical Trim | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L10-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L15-8120 | Bathrooms - Install Countertops | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 10-Dec-14 A | 16-Dec-14 A | |
| L11-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 10-Dec-14 A | 24-Dec-14 A | |
| L04-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 11-Dec-14 A | 05-Feb-15 A | |
| L04-8134 | Final Clean @ Guestrooms | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L05-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 12-Dec-14 A | 10-Feb-15 A | |
| L05-8134 | Final Clean @ Guestrooms | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L11-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 12-Dec-14 A | 17-Dec-14 A | |
| L06-8134 | Final Clean @ Guestrooms | 5 | 0 | 13-Dec-14 A | 13-Dec-14 A | |
| L12-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 15-Dec-14 A | 18-Dec-14 A | |
| L17-8124 | Install Flooring | 5 | 0 | 15-Dec-14 A | 18-Dec-14 A | |

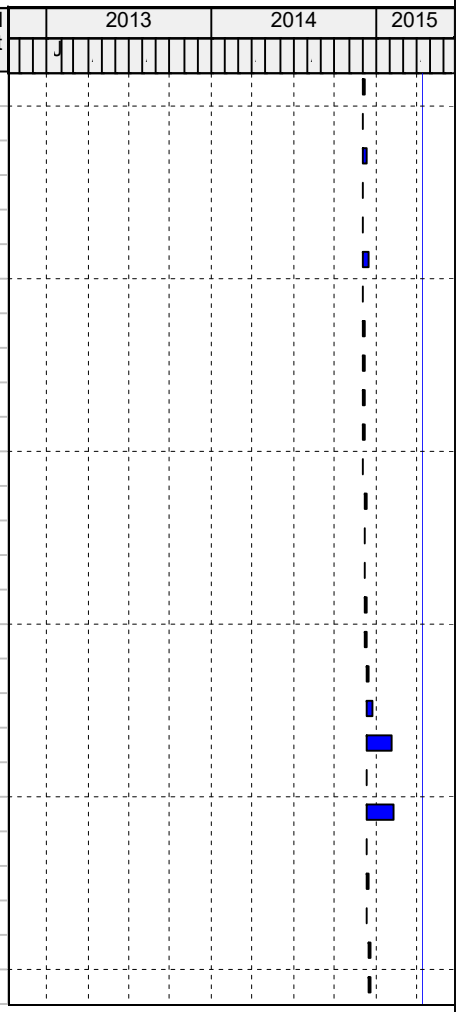



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8116 | Install Base and Door Thresholds | 5 | 0 | 18-Dec-14 A | 30-Dec-14 A | |
| L12-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| L14-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| L15-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 29-Dec-14 A | 05-Jan-15 A | |
| L16-8120 | Bathrooms - Install countertops | 3 | 0 | 29-Dec-14 A | 09-Jan-15 A | |
| L14-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 30-Dec-14 A | 05-Jan-15 A | |
| L15-8122 | Bathrooms - Plumbing fixtures & trim | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L16-8128 | Bathrooms - Install shower/tub surrounds | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L16-8122 | Bathrooms - Plumbing fixtures & trim | 3 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8128 | Bathrooms - Install shower/tub surrounds | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L09-8110 | HVAC grilles & registers | 2 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| L11-8110 | HVAC grilles & registers | 2 | 0 | 21-Jan-15 A | 28-Jan-15 A | |
| L12-8110 | HVAC grilles & registers | 2 | 0 | 21-Jan-15 A | 28-Jan-15 A | |
| L14-8110 | HVAC grilles & registers | 2 | 0 | 21-Jan-15 A | 02-Feb-15 A | |
| L10-8110 | HVAC grilles & registers | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L15-8110 | HVAC grilles & registers | 2 | 0 | 03-Feb-15 A | 16-Feb-15 A | |
| L16-8110 | HVAC grilles & registers | 2 | 0 | 03-Feb-15 A | 23-Feb-15 A | |
| L17-8122 | Bathrooms - Plumbing fixtures & trim | 3 | 1 | 03-Feb-15 A | 14-Apr-15 | 12 |
| L17-8120 | Bathrooms - Install countertops | 3 | 1 | 03-Feb-15 A | 13-Apr-15 | 12 |
| L06-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 04-Feb-15 A | 12-Feb-15 A | |
| L07-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 06-Feb-15 A | 20-Feb-15 A | |
| L14-8107 | Paint, final coat & touch-up | 3 | 0 | 09-Feb-15 A | 11-Feb-15 A | |
| L17-8110 | HVAC grilles & registers | 2 | 0 | 09-Feb-15 A | 31-Mar-15 A | |
| L08-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 10-Feb-15 A | 07-Mar-15 A | |
| L09-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 12-Feb-15 A | 06-Mar-15 A | |
| L15-8107 | Paint, final coat & touch-up | 3 | 0 | 16-Feb-15 A | 18-Feb-15 A | |
| L10-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 18-Feb-15 A | 13-Mar-15 A | |

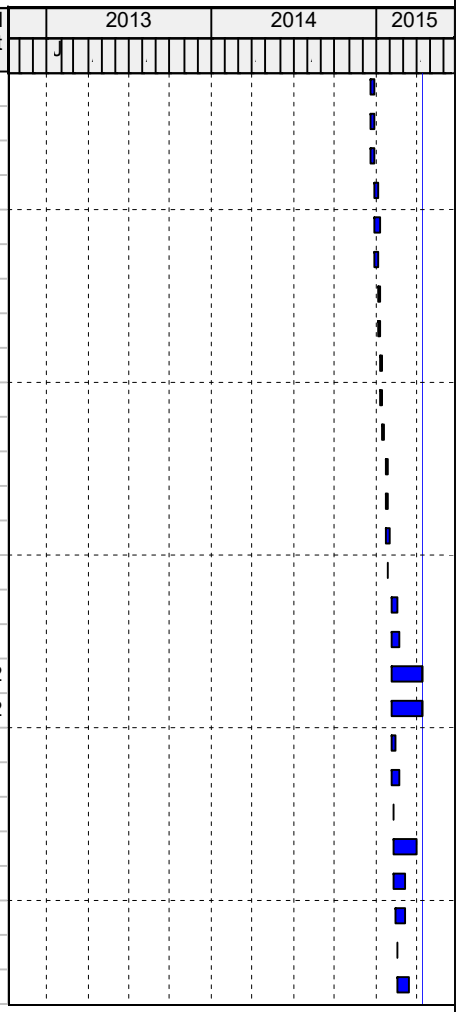


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8132 | Contractor Punchlist (inspect/distribute/correct/back-pı | 7 | 0 | 20-Feb-15 A | 20-Mar-15 A | |
| L16-8107 | Paint, final coat & touch-up | 3 | 0 | 24-Feb-15 A | 26-Feb-15 A | |
| L12-8132 | Contractor Punchlist (inspect/distribute/correct/back-pı | 7 | 0 | 25-Feb-15 A | 25-Mar-15 A | |
| L14-8132 | Contractor Punchlist (inspect/distribute/correct/back-pı | 7 | 0 | 26-Feb-15 A | 27-Mar-15 A | |
| L03-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L04-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L05-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L06-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L07-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L08-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L09-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L10-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L11-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L12-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L14-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L15-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L16-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L17-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L15-8132 | Contractor Punchlist (inspect/distribute/correct/back-pı | 7 | 0 | 06-Mar-15 A | 06-Apr-15 A | |
| L16-8132 | Contractor Punchlist (inspect/distribute/correct/back-pı | 7 | 0 | 10-Mar-15 A | 08-Apr-15 A | |
| L17-8107 | Paint, final coat & touch-up | 2 | 0 | 25-Mar-15 A | 26-Mar-15 A | |
| L03-8132 | Contractor Punchlist (inspect/distribute/correct/back-pı | 5 | 5 | 13-Apr-15 | 17-Apr-15 | 30 |
| L17-8132 | Contractor Punchlist (inspect/distribute/correct/back-pı | 5 | 5 | 16-Apr-15 | 22-Apr-15 | 12 |
| **Pool Area** | | | | | | |
| L03-8216 | Install pool tile, coping and depth markers | 5 | 5 | 21-Apr-15 | 27-Apr-15 | 1 |
| **Corridors / Common / Public Areas** | | | | | | |
| L03-8200 | Vinyl Wall Coverings | 3 | 0 | 01-Aug-14 A | 05-Aug-14 A | |

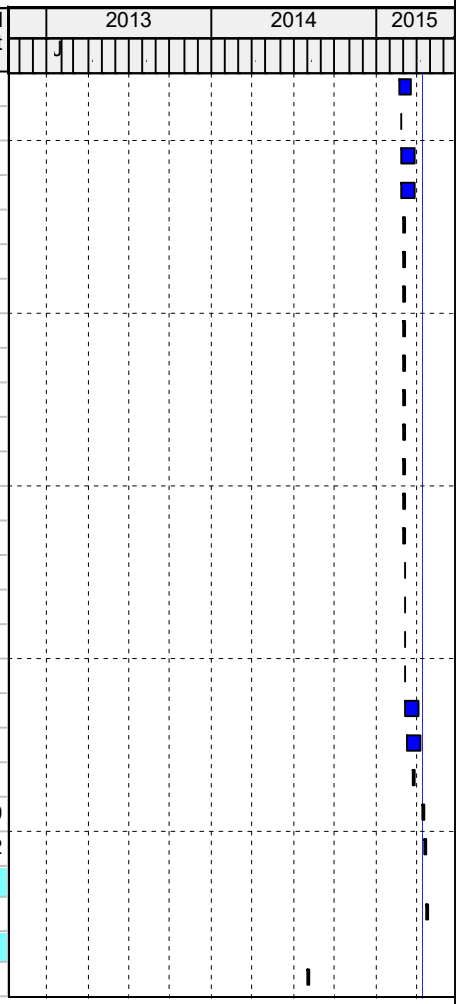



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8200 | Vinyl Wall Coverings | 5 | 0 | 06-Aug-14 A | 12-Aug-14 A | |
| L05-8200 | Vinyl Wall Coverings | 5 | 0 | 12-Aug-14 A | 22-Sep-14 A | |
| L03-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L06-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L08-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 11-Sep-14 A | 19-Sep-14 A | |
| L04-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| L05-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L06-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L07-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L09-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| L10-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 08-Oct-14 A | |
| L11-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 10-Oct-14 A | |
| L08-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L12-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| L09-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L14-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 16-Oct-14 A | 27-Oct-14 A | |
| L10-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |
| L11-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L15-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 22-Oct-14 A | 29-Oct-14 A | |
| L12-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 03-Nov-14 A | 04-Nov-14 A | |
| L14-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L15-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 05-Nov-14 A | 06-Nov-14 A | |
| L16-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 14-Nov-14 A | 20-Nov-14 A | |
| L16-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L17-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L17-8200 | Wall coverings - vinyl at window niches & outside batl | 4 | 0 | 15-Dec-14 A | 24-Mar-15 A | |

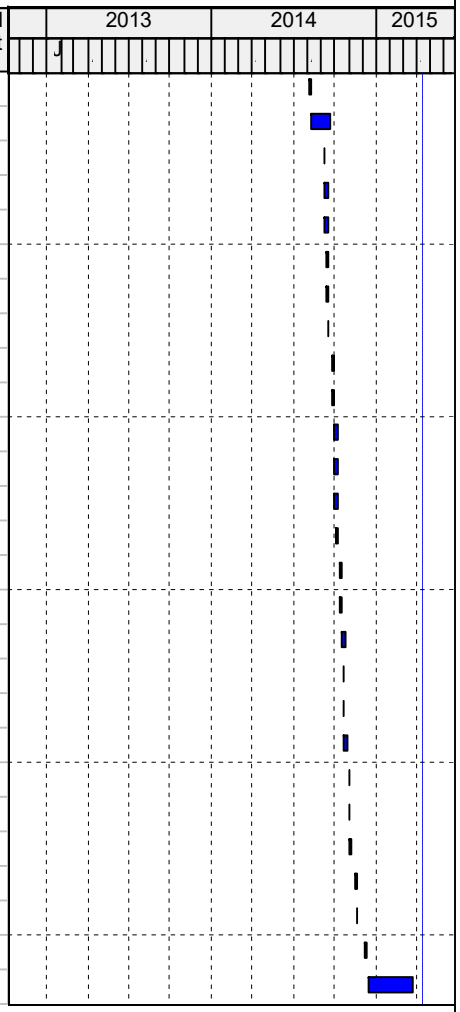


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8206 | Flooring - carpet at corridors | 2 | 0 | 14-Jan-15 A | 23-Jan-15 A | |
| L05-8206 | Flooring - carpet at corridors | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| L07-8206 | Flooring - carpet at corridors | 2 | 0 | 22-Jan-15 A | 23-Jan-15 A | |
| L06-8206 | Flooring - carpet at corridors | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L09-8206 | Flooring - carpet at corridors | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| L08-8206 | Flooring - carpet at corridors | 2 | 0 | 04-Feb-15 A | 05-Feb-15 A | |
| L10-8206 | Flooring - carpet at corridors | 2 | 0 | 06-Feb-15 A | 09-Feb-15 A | |
| L11-8206 | Flooring - carpet at corridors | 2 | 0 | 10-Feb-15 A | 11-Feb-15 A | |
| L12-8206 | Flooring - carpet at corridors | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| L04-8208 | Final Cleaning | 2 | 0 | 13-Feb-15 A | 16-Feb-15 A | |
| L14-8206 | Flooring - carpet at corridors | 2 | 0 | 13-Feb-15 A | 14-Feb-15 A | |
| L15-8206 | Flooring - carpet at corridors | 2 | 0 | 16-Feb-15 A | 17-Feb-15 A | |
| L04-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 17-Feb-15 A | 03-Mar-15 A | |
| L05-8208 | Final Cleaning | 2 | 0 | 17-Feb-15 A | 18-Feb-15 A | |
| L05-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 18-Feb-15 A | 05-Mar-15 A | |
| L16-8206 | Flooring - carpet at corridors | 2 | 0 | 18-Feb-15 A | 19-Feb-15 A | |
| L06-8208 | Final Cleaning | 2 | 0 | 20-Feb-15 A | 25-Feb-15 A | |
| L03-8206 | Flooring - carpet at corridors (N-S leg) | 2 | 0 | 25-Feb-15 A | 25-Feb-15 A | |
| L06-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 4 | 0 | 25-Feb-15 A | 10-Mar-15 A | |
| L07-8208 | Final Cleaning | 2 | 0 | 27-Feb-15 A | 02-Mar-15 A | |
| L04-8214 | Floor Complete | 0 | 0 | | 03-Mar-15 A | |
| L07-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 05-Mar-15 A | 18-Mar-15 A | |
| L08-8208 | Final Cleaning | 2 | 0 | 05-Mar-15 A | 06-Mar-15 A | |
| L05-8214 | Floor Complete | 0 | 0 | | 05-Mar-15 A | |
| L08-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 06-Mar-15 A | 25-Mar-15 A | |
| L06-8214 | Floor Complete | 0 | 0 | | 10-Mar-15 A | |
| L09-8208 | Final Cleaning | 2 | 0 | 12-Mar-15 A | 13-Mar-15 A | |

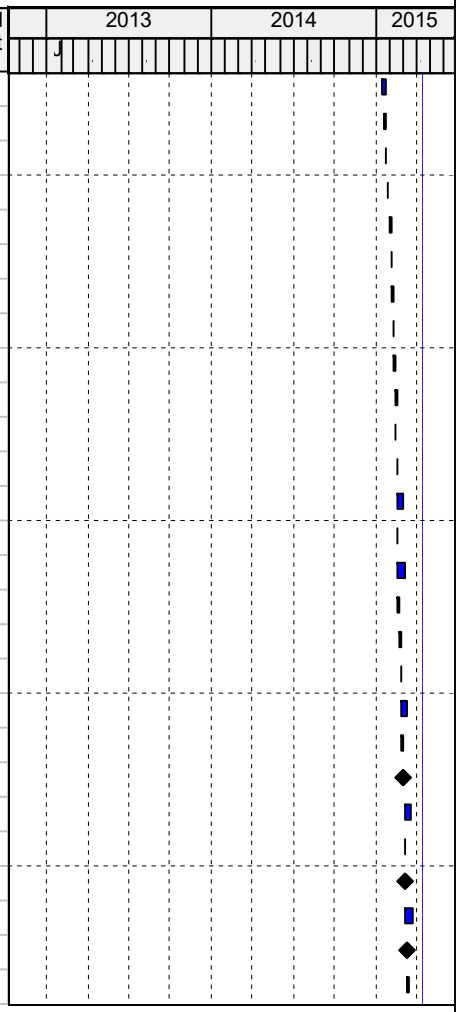



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 12-Mar-15 A | 25-Mar-15 A | |
| L07-8214 | Floor Complete | 0 | 0 | | 18-Mar-15 A | |
| L10-8208 | Final Cleaning | 2 | 0 | 19-Mar-15 A | 20-Mar-15 A | |
| L10-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 9 | 0 | 23-Mar-15 A | 06-Apr-15 A | |
| L11-8208 | Final Cleaning | 2 | 0 | 23-Mar-15 A | 24-Mar-15 A | |
| L11-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 8 | 0 | 24-Mar-15 A | 06-Apr-15 A | |
| L08-8214 | Floor Complete | 0 | 0 | | 25-Mar-15 A | |
| L09-8214 | Floor Complete | 0 | 0 | | 25-Mar-15 A | |
| L12-8208 | Final Cleaning | 2 | 0 | 26-Mar-15 A | 27-Mar-15 A | |
| L12-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 9 | 0 | 31-Mar-15 A | 09-Apr-15 A | |
| L14-8208 | Final Cleaning | 2 | 0 | 31-Mar-15 A | 01-Apr-15 A | |
| L17-8206 | Flooring - carpet at corridors | 2 | 0 | 31-Mar-15 A | 01-Apr-15 A | |
| L14-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 7 | 0 | 06-Apr-15 A | 09-Apr-15 A | |
| L15-8208 | Final Cleaning | 2 | 0 | 06-Apr-15 A | 07-Apr-15 A | |
| L10-8214 | Floor Complete | 0 | 0 | | 06-Apr-15 A | |
| L11-8214 | Floor Complete | 0 | 0 | | 06-Apr-15 A | |
| L15-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 9 | 4 | 08-Apr-15 A | 16-Apr-15 | 24 |
| L16-8208 | Final Cleaning | 2 | 0 | 09-Apr-15 A | 10-Apr-15 A | |
| L12-8214 | Floor Complete | 0 | 0 | | 09-Apr-15 A | |
| L14-8214 | Floor Complete | 0 | 0 | | 09-Apr-15 A | |
| L16-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 7 | 4 | 10-Apr-15 A | 16-Apr-15 | 24 |
| L15-8214 | Floor Complete | 0 | 0 | | 16-Apr-15 | 24 |
| L16-8214 | Floor Complete | 0 | 0 | | 16-Apr-15 | 24 |
| L03-8208 | Final Cleaning | 2 | 2 | 20-Apr-15 | 21-Apr-15 | 30 |
| L03-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 5 | 21-Apr-15 | 27-Apr-15 | 30 |
| L17-8208 | Final Cleaning | 2 | 2 | 23-Apr-15 | 24-Apr-15 | 12 |
| L17-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 7 | 7 | 24-Apr-15 | 04-May-15 | 12 |

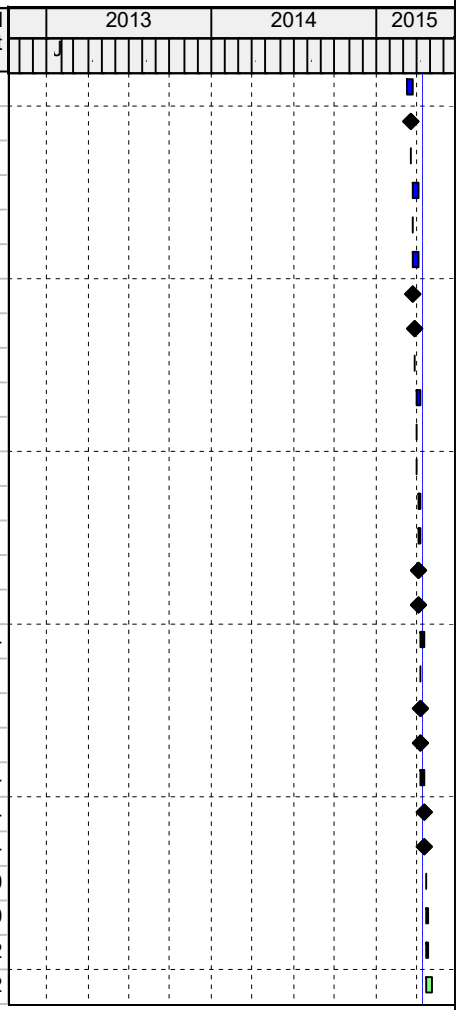



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8214 | Floor Complete | 0 | 0 | | 04-May-15 | 12 |
| L03-8214 | Floor Complete | 0 | 0 | | 03-Jun-15 | 4 |
| **Mech Penthouse** | | | | | | |
| PH-8100 | PH - Insulation & Vapor Barrier | 5 | 0 | 09-Oct-14 A | 13-Oct-14 A | |
| PH-8102 | PH - Complete GWB Hang / Tape / Finish | 6 | 0 | 14-Oct-14 A | 10-Nov-14 A | |
| PH-8122 | PH - Plumbing Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8110 | PH - HVAC Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8126 | PH - install doors & hardware | 2 | 0 | 24-Nov-14 A | 23-Feb-15 A | |
| PH-8104 | PH - Int Painting [DELETED] | 4 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| PH-8108 | PH - Elec Trim / Finish | 5 | 0 | 01-Dec-14 A | 19-Jan-15 A | |
| PH-8114 | PH - Install Stairs to Roof [DELETED] | 1 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| PH-8118 | PH - Fire Alarm Trim (speaker/strobe & smoke detecto | 5 | 0 | 01-Dec-14 A | 21-Jan-15 A | |
| PH-8124 | PH - Flooring [DELETED, NIC] | 5 | 0 | 01-Jan-15 A | 01-Jan-15 A | |
| PH-8134 | PH - Final Trims and Touch-Up | 3 | 0 | 16-Mar-15 A | 18-Mar-15 A | |
| PH-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 04-May-15 | 08-May-15 | 5 |
| PH-8208 | Final Cleaning | 2 | 2 | 11-May-15 | 12-May-15 | 5 |
| PH-8212 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 13-May-15 | 15-May-15 | 5 |
| PH-8214 | Penthouse Complete | 0 | 0 | | 15-May-15 | 5 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| **Smoke Control** | | | | | | |
| CO-7104 | Fire Alarm/Smoke Control Pre-Functional Testing - Po | 13 | 13 | 27-Apr-15 | 13-May-15 | 0 |
| CO-7106 | City of Bellevue Smoke Control Functional Acceptanc | 6 | 6 | 13-May-15 | 20-May-15 | 0 |
| CO-7108 | Final Marriott Smoke Control Funcational Acceptance | 2 | 2 | 21-May-15 | 22-May-15 | 0 |
| **Fire Sprinklers** | | | | | | |
| CO-7114 | Marriott Fire Sprinkler Funcational Acceptance Testing | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7110 | Fire Sprinkler Pre-Testing (Podium) | 3 | 0 | 26-Mar-15 A | 26-Mar-15 A | |

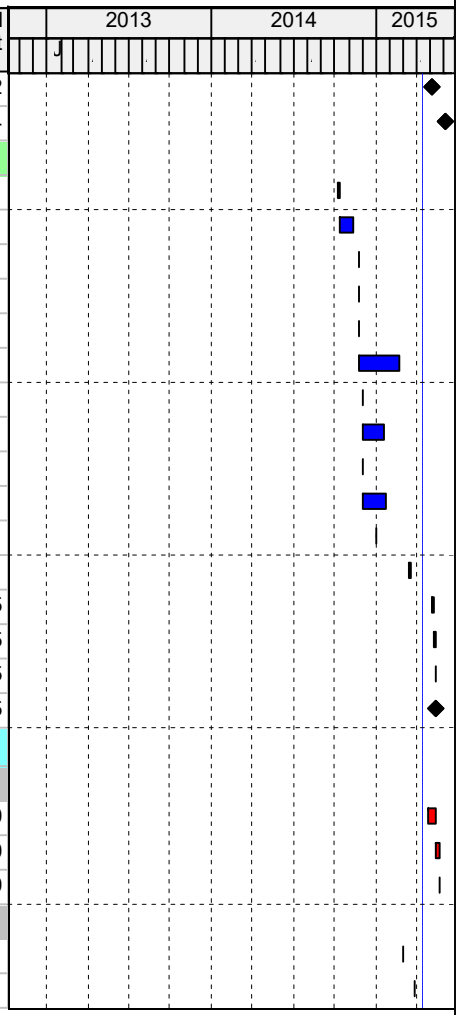



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7112 | City of Bellevue Fire Sprinkler Final Inspection | 6 | 6 | 13-May-15 | 20-May-15 | 0 |
| **Fire Alarm** | | | | | | |
| CO-7116 | Fire Alarm Pre-Testing (Podium) [DELETED] | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7118 | City of Bellevue Fire Alarm Functional Acceptance Tes | 6 | 6 | 13-May-15 | 20-May-15 | 0 |
| CO-7120 | Marriott Fire Alarm Funcational Acceptance Testing | 2 | 2 | 21-May-15 | 22-May-15 | 0 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| CO-7100 | Cx - Start-Up - Garage Exhaust Fan and VFD's | 4 | 0 | 30-Mar-15 A | 02-Apr-15 A | |
| CO-7102 | Cx - DDC Point-To-Point - Garage Exhaust Fans [DEL | 5 | 0 | 01-Apr-15 A | 01-Apr-15 A | |

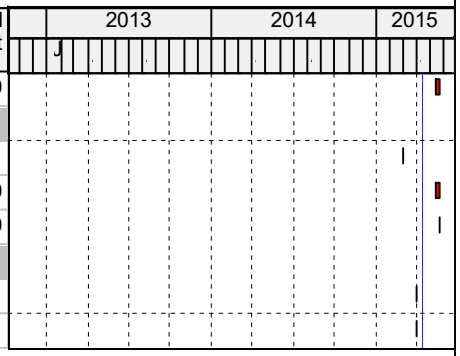



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Working Schedule - 5-17-15 Update** | | | | | | |
| I-4500 | Re-design building exterior (change from EIFS panels | 30 | 0 | 12-Apr-13 A | 28-May-14 A | |
| ASI01 | ASI No. 1 - Tower Crane Foundation Changes | 0 | 0 | 09-May-13 A | | |
| I-2292 | RFI 233/ Original HVAC submittal with specified damp | 1 | 0 | 13-May-13 A | 12-Jun-13 A | |
| ASI03 | ASI No. 3 - Food Service Plans and Cut Sheets | 0 | 0 | 14-May-13 A | | |
| ASI04 | ASI No. 4 - Revised Structural For The Podium | 0 | 0 | 22-May-13 A | | |
| ASI05 | ASI No. 5 - NTI Drawings | 0 | 0 | 22-May-13 A | | |
| I-1500 | Owner release revised LV design - Tower (ASIs 5, 13, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-1550 | Owner release revised LV design - Podium (ASIs 5, 1 | 200 | 0 | 23-May-13 A | 28-Apr-14 A | |
| I-1900 | Owner issue design revisions (ASIs 4, 9, 19, 34) | 215 | 0 | 23-May-13 A | 24-Mar-14 A | |
| I-2500 | Owner issue LL1 electrical revisions (ASIs 7, 9r2, 14, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| ASI02 | ASI No. 2 - Foundation Drainage System | 0 | 0 | 05-Jun-13 A | | |
| ASI04c | ASI No. 4 - Revised Structural For The Podium (Clouc | 0 | 0 | 05-Jun-13 A | | |
| ASI07 | ASI No. 7 - Electrical Rev-10 Changes | 0 | 0 | 18-Jun-13 A | | |
| ASI06 | ASI No. 6 - Mechanical Rev-8 Changes | 0 | 0 | 19-Jun-13 A | | |
| I-3700 | Owner resolve wall condition between stair and Eleva | 200 | 0 | 27-Jun-13 A | 16-Jun-14 A | |
| MM-1000 | MM - Temporary Power Available | 0 | 0 | 08-Jul-13 A | | |
| I-2100 | Owner revise roof steel design (Submittals 365, 370, | 200 | 0 | 09-Jul-13 A | 07-Apr-14 A | |
| I-2200 | Owner resolve elevator steel issue (RFI 112, RFI 112. | 200 | 0 | 09-Jul-13 A | 03-Mar-14 A | |
| I-2400 | Owner provide Tower light fixture selections (ASI 36) | 185 | 0 | 18-Jul-13 A | 08-Apr-14 A | |
| I-3400 | Owner provide Level 2 ceiling heights (RFI 465) | 180 | 0 | 19-Jul-13 A | 01-Jul-14 A | |
| I-2294 | RFI 233/ Revised HVAC submittal | 1 | 0 | 22-Jul-13 A | 25-Jul-13 A | |
| ASI04ca | ASI No. 4 - Revised Structural For The Podium (City A | 0 | 0 | 05-Aug-13 A | | |
| ASI11 | ASI No. 11 - Food and Beverage Drawing Revisions | 0 | 0 | 05-Aug-13 A | | |
| I-2900 | Owner revise Food Service and Kitchen (ASIs 11, 12, | 140 | 0 | 08-Aug-13 A | 27-Feb-14 A | |
| ASI12 | ASI No. 12 - Food and Beverage Drawing Changes | 0 | 0 | 12-Aug-13 A | | |
| ASI08 | ASI No. 8 - Provent System | 0 | 0 | 15-Aug-13 A | | |

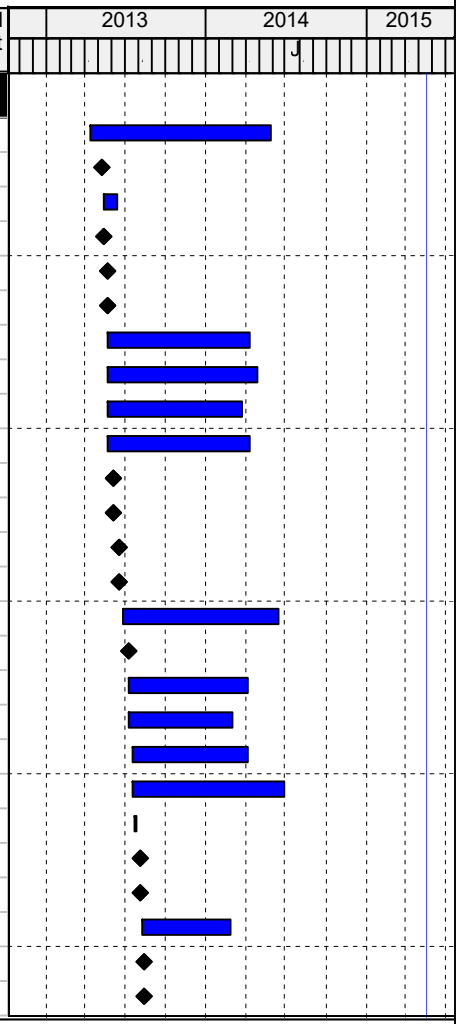


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-5010 | RFI 173 - Porte Cochere Bench Design | 1 | 0 | 16-Aug-13 A | 04-Sep-13 A | |
| I-5012 | RFI 189 - Porte Cochere Pavement Design | 1 | 0 | 26-Aug-13 A | 30-Jun-14 A | |
| I-1400 | Owner develop envelope redesign | 70 | 0 | 27-Aug-13 A | 12-Dec-13 A | |
| I-5014 | RFI 197 - LL1 & LL2 Planter Drain Pipes | 1 | 0 | 03-Sep-13 A | 06-Sep-13 A | |
| I-3600 | Owner closeout glass/glazing allowance | 160 | 0 | 04-Sep-13 A | 30-Apr-14 A | |
| ASI09 | ASI No. 9 - Incorporating Arch, MEP & Struct Drawing | 0 | 0 | 05-Sep-13 A | | |
| I-1200 | Owner release revised Concierge Lounge design (AS | 160 | 0 | 06-Sep-13 A | 22-Oct-14 A | |
| ASI13 | ASI No. 13 - NTI Drawing Updates | 0 | 0 | 06-Sep-13 A | | |
| I-2800 | Owner revise interior public space design (ASIs 16, 1 | 130 | 0 | 25-Sep-13 A | 09-Apr-14 A | |
| ASI16 | ASI No. 16 - 9.20..13 General ID Releasae | 0 | 0 | 25-Sep-13 A | | |
| I-2296 | RFI 233/ Issue RFI and receive response | 1 | 0 | 25-Sep-13 A | 21-Jan-14 A | |
| I-2000 | Owner approve door frames (Submittals 258, 454, 48 | 85 | 0 | 27-Sep-13 A | 23-Jan-14 A | |
| ASI14 | ASI No. 14 - Electrical Revisions for Low Voltage | 0 | 0 | 04-Oct-13 A | | |
| ASI17 | ASI No. 17 - Smoke Control Design 42C Permit | 0 | 0 | 09-Oct-13 A | | |
| ASI18 | ASI No. 18 - Interior Package Revisions | 0 | 0 | 15-Oct-13 A | | |
| I-3100 | Owner revise ballroom ceiling design (ASIs 18, 25) | 100 | 0 | 17-Oct-13 A | 25-Feb-14 A | |
| I-1600 | Owner provide directive for south & east corridor encl | 110 | 0 | 28-Oct-13 A | 18-Apr-14 A | |
| I-5016 | RFI 282 - Porte Cochere Planter Dimensions | 1 | 0 | 01-Nov-13 A | 21-Jan-14 A | |
| ASI11-12 | ASI No. 11 & 12 - Kitchen Equipment Specifications | 0 | 0 | 06-Nov-13 A | | |
| ASI09r1s | ASI No. 9 (Revised) - City Approved ASI No. 9 (Struct | 0 | 0 | 07-Nov-13 A | | |
| I-2600 | Owner resolve L2 slab coordination issue | 4 | 0 | 13-Nov-13 A | 16-Nov-13 A | |
| ASI09r1m | ASI No. 9 (Revised) - City Approved ASI No. 9 (Mecha | 0 | 0 | 15-Nov-13 A | | |
| ASI06r1 | ASI No. 6 (Revised) - Mechanical Rev-8 Changes (Cit | 0 | 0 | 19-Nov-13 A | | |
| ASI21 | ASI No. 21 - Revised Structural Drawings for the Roof | 0 | 0 | 22-Nov-13 A | | |
| I-2700 | Owner revise tower guest rooms design (ASIs 23, 29) | 58 | 0 | 04-Dec-13 A | 26-Feb-14 A | |
| ASI09r1e | ASI No. 9 (Revised) - ASI No. 9 Electrical Drawings (R | 0 | 0 | 04-Dec-13 A | | |
| ASI20 | ASI No. 20 - Dry Utilities Revisions | 0 | 0 | 05-Dec-13 A | | |

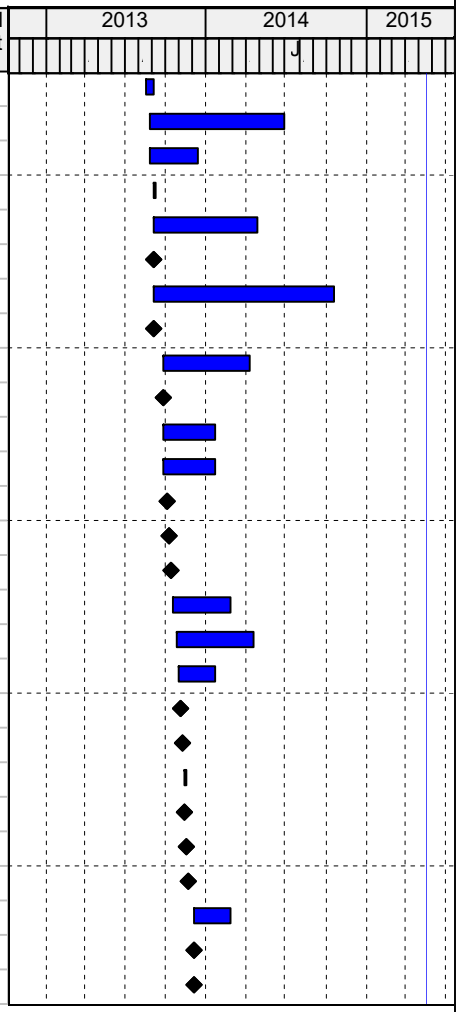


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1700 | Owner provide design for dry site utilities (ASIs 20, 20 | 66 | 0 | 09-Dec-13 A | 13-Mar-14 A | |
| I-1402 | Begin exterior panel production | 41 | 0 | 13-Dec-13 A | 12-Feb-14 A | |
| ASI17ca | ASI No. 17 - Smoke Control Design 42C Permit (City / | 0 | 0 | 16-Dec-13 A | | |
| ASI09r2e | ASI No. 9 (Revised) - ASI No. 9 Electrical Drawings (R | 0 | 0 | 18-Dec-13 A | | |
| I-1300 | Owner issue "Hold" directive (email) | 0 | 0 | | 19-Dec-13 A | |
| ASI22 | ASI No. 22 - Revised Door Schedule and Door Hardw | 0 | 0 | 19-Dec-13 A | | |
| I-1100 | Owner release revised L17 design (ASI 23, 29R1) | 74 | 0 | 20-Dec-13 A | 08-Apr-14 A | |
| I-1302 | Owner issue ASI 30 (Prep Kitchen Revisions) | 47 | 0 | 20-Dec-13 A | 27-Feb-14 A | |
| ASI23 | ASI No. 23 - Revised Tower and Enlarged Guestroom | 0 | 0 | 20-Dec-13 A | | |
| I-1404 | City of Bellevue Approval | 90 | 0 | 23-Dec-13 A | 15-Jul-14 A | |
| I-5470 | Resolve ceiling height issue at Laundy Room (RFI __ | 5 | 0 | 05-Jan-14 A | 30-Jan-15 A | |
| ASI15 | ASI No. 15 - NTI DV Drawings Revisions | 0 | 0 | 08-Jan-14 A | | |
| ASI09R2e2 | ASI No. 9 (Revised) - City Approved ASI No. 9 (Electri | 0 | 0 | 14-Jan-14 A | | |
| ASI22r1 | ASI No. 22 (Revised) - Architectural Revisions to Door | 0 | 0 | 20-Jan-14 A | | |
| I-3000 | ASI 38/ Owner revise bar area (change to straight bai | 71 | 0 | 22-Jan-14 A | 27-May-14 A | |
| I-2298 | RFI 233/ Resolve issue with designer & City | 1 | 0 | 22-Jan-14 A | 14-Mar-14 A | |
| ASI20r1 | ASI No. 20 (Revised) - Dry Utilities Revsions | 0 | 0 | 23-Jan-14 A | | |
| ASI24 | ASI No. 24 - FRCH ID Finish Schedule | 0 | 0 | 30-Jan-14 A | | |
| ASI26 | ASI No. 26 - Revised Laundry Layout and Equipment | 0 | 0 | 12-Feb-14 A | | |
| I-1306 | Prep Kitchen - Additional plumbing (ASI 30) | 4 | 0 | 17-Feb-14 A | 01-Aug-14 A | |
| ASI28 | ASI No. 28 - Guest Laundry Equipment Sheets | 0 | 0 | 20-Feb-14 A | | |
| ASI27 | ASI No. 27 - Mechanical, Electrical and Plumbing She | 0 | 0 | 21-Feb-14 A | | |
| ASI25 | ASI No. 25 - Podium Level Revisions (Stair 1 & 2 Gat | 0 | 0 | 24-Feb-14 A | | |
| ASI29 | ASI No. 29 - Architectural Tower and Guestroom Revi | 0 | 0 | 26-Feb-14 A | | |
| ASI30 | ASI No. 30 - Food Service Revisions per HEI | 0 | 0 | 27-Feb-14 A | | |
| I-2202 | Fabricate revised elevator steel | 60 | 0 | 04-Mar-14 A | 07-May-14 A | |
| I-2704 | Framing "Go Back" work for ASIs 23, 29 - L4 | 1 | 0 | 05-Mar-14 A | 12-Mar-14 A | |

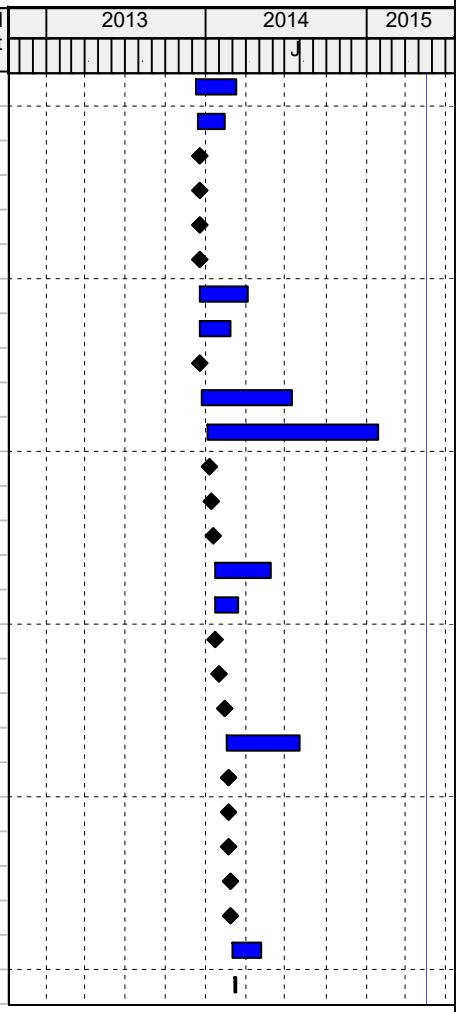



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ASI31 | ASI No. 31 - Revised Elevations | 0 | 0 | 07-Mar-14 A | | |
| ASI33 | ASI No. 33 - NTI DV Drawing Revisions | 0 | 0 | 11-Mar-14 A | | |
| ASI20r2 | ASI No. 20 (Revised) - Dry Utilities Revisions | 0 | 0 | 13-Mar-14 A | | |
| I-1702 | Owner provide directive to proceed | 26 | 0 | 14-Mar-14 A | 01-May-14 A | |
| I-2300 | RFI 233/ Procure dampers | 1 | 0 | 15-Mar-14 A | 11-Apr-14 A | |
| I-3300 | Owner provide Guest Room plumbing fixture selectio | 1 | 0 | 20-Mar-14 A | 20-Mar-14 A | |
| ASI34 | ASI No. 34 - SCA Structural Revisions S6.01 and S6.( | 0 | 0 | 24-Mar-14 A | | |
| I-4600 | RFI 72, HHP3-HHP5 - resolve electrical issue & revise | 1 | 0 | 24-Mar-14 A | 09-Apr-14 A | |
| I-1902 | Procure revised structural steel | 15 | 0 | 25-Mar-14 A | 14-Apr-14 A | |
| I-3900 | Ballroom Parapet Height Issue/ RFI 471 | 1 | 0 | 28-Mar-14 A | 07-May-14 A | |
| I-3016 | ASI 38/ Scan Level 1 slab at bar (3 times) | 1 | 0 | 31-Mar-14 A | 11-Apr-14 A | |
| I-4000 | Owner complete design of east stitched enclosure (fo | 1 | 0 | 01-Apr-14 A | 14-May-14 A | |
| ASI35 | ASI No. 35 - FRCH ID Revisions and Finish Schedule | 0 | 0 | 07-Apr-14 A | | |
| I-2102 | Fabricate revised roof steel | 20 | 0 | 08-Apr-14 A | 15-May-14 A | |
| I-3200 | Owner provide light fixture selections for podium level | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| ASI36 | ASI No. 36 - MDP Electrical Revisions Rev. 16 | 0 | 0 | 08-Apr-14 A | | |
| ASI29r1 | ASI No. 29 (Revised) - Guestroom, Interior Elevation, | 0 | 0 | 09-Apr-14 A | | |
| I-3800 | Resolve  Heat Pump Electrical Overcurrent Issue | 20 | 0 | 23-Apr-14 A | 18-Jun-14 A | |
| L10-8221 | HVAC Risers Duct Insulation | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L11-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| ASI37 | ASI No. 37 - NTI DV Drawing Revisions | 0 | 0 | 28-Apr-14 A | | |
| I-2304 | RFI 233/ Framing "Go Back" work at L3 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2306 | RFI 233/ Framing "Go Back" work at L4 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2308 | RFI 233/ Framing "Go Back" work at L5 | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2706 | Framing "Go Back" work for ASIs 23, 29 - L5 | 1 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2708 | Framing "Go Back" work for ASIs 23, 29 - L6 | 1 | 0 | 29-Apr-14 A | 09-May-14 A | |

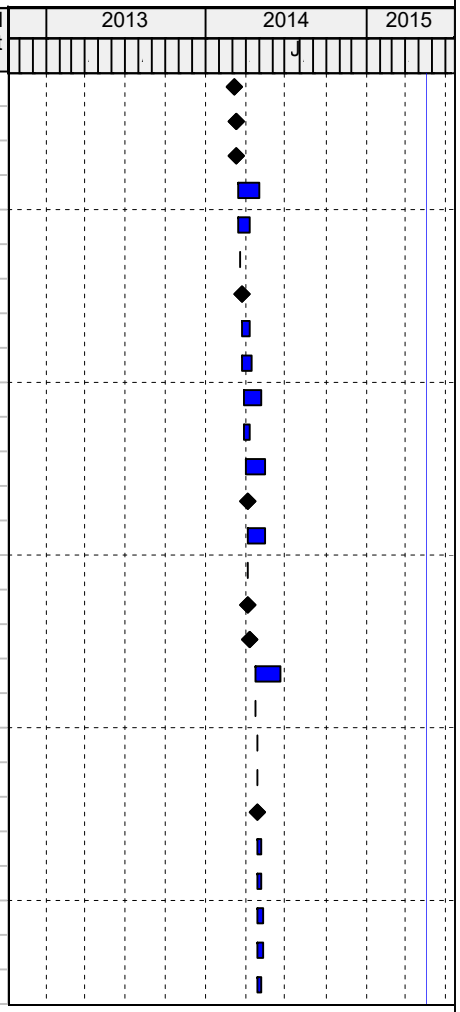



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-2702 | Framing "Go Back" work for ASIs 23, 29 - L3 | 1 | 0 | 01-May-14 A | 01-May-14 A | |
| I-1706 | PSE scheduling delay | 10 | 0 | 01-May-14 A | 20-May-14 A | |
| I-3602 | Complete shop drawings & fab/deliver storefront fram | 40 | 0 | 01-May-14 A | 14-Jun-14 A | |
| L04-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| I-3904 | Ballroom Parapet Height Issue/ re-engineer parapet | 1 | 0 | 06-May-14 A | 01-Jul-14 A | |
| I-1802 | Rework framing for door hold-opens - LL4 | 1 | 0 | 07-May-14 A | 08-May-14 A | |
| L04-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-May-14 A | 12-May-14 A | |
| ASI25r1 | ASI No. 25 (Revised) - Architectural Podium Level Re | 0 | 0 | 07-May-14 A | | |
| ASI29r2 | ASI No. 29 (Revised) - Architectural Tower and Guestı | 0 | 0 | 07-May-14 A | | |
| I-1800 | Owner issue directive to proceed with door hold-open | 1 | 0 | 08-May-14 A | 08-May-14 A | |
| I-1804 | Rework framing for door hold-opens - LL3 | 1 | 0 | 08-May-14 A | 09-May-14 A | |
| I-2312 | RFI 233/ Framing "Go Back" work at L7 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-2314 | RFI 233/ Framing "Go Back" work at L8 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-3902 | Install Ballroom parapet extension | 5 | 0 | 08-May-14 A | 13-May-14 A | |
| I-1806 | Rework framing for door hold-opens - LL2 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-1808 | Rework framing for door hold-opens - LL1 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-2310 | RFI 233/ Framing "Go Back" work at L6 | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| I-2710 | Framing "Go Back" work for ASIs 23, 29 - L7 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| L05-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L06-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L05-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| LL2E-8110 | LL2 - Electrical, Fire pumps/equipment final connectic | 5 | 0 | 12-May-14 A | 30-Oct-14 A | |
| I-2316 | RFI 233/ Install dampers | 1 | 0 | 12-May-14 A | 15-May-14 A | |
| PH-8704 | PH - Install Machine Support Steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| PH-8710 | Install elevator rail support steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| L03-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 13-May-14 A | 14-May-14 A | |

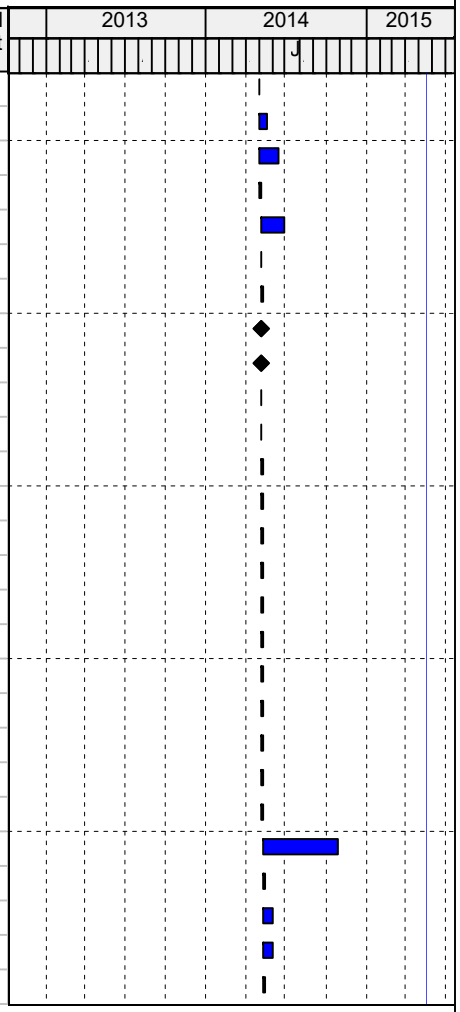



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 13-May-14 A | 14-May-14 A | |
| I-2318 | RFI 233/ Install dampers | 1 | 0 | 15-May-14 A | 19-May-14 A | |
| I-4002 | East Stitched - Install framing and windows | 9 | 0 | 19-May-14 A | 09-Jun-14 A | |
| I-2320 | RFI 233/ Install dampers | 1 | 0 | 20-May-14 A | 26-May-14 A | |
| L10-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L11-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L12-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| RF-4038 | AR - Concrete pads and curbs | 5 | 0 | 21-May-14 A | 04-Jun-14 A | |
| ASI27cap | ASI No. 27 - City Approved ASI No. 27 (Plumbing) | 0 | 0 | 21-May-14 A | | |
| ASI38 | ASI No. 38 - MDP's Bar & Concierge Plumbing Revisi | 0 | 0 | 22-May-14 A | | |
| L10-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L11-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L12-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L14-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L15-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 27-May-14 A | |
| L11-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 07-Jun-14 A | |
| L12-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 27-May-14 A | 06-Jun-14 A | |
| I-2322 | New Activity | 1 | 0 | 27-May-14 A | 28-May-14 A | |
| I-3002 | ASI 38/ City of Bellevue approve bar design changes | 5 | 0 | 28-May-14 A | 12-Dec-14 A | |
| I-4502 | Release metal panels for fabrication | 0 | 0 | 28-May-14 A | | |
| I-4504 | Metal panel fabrication (1st delivery) | 1 | 0 | 29-May-14 A | 08-Jul-14 A | |
| I-2324 | RFI 233/ Install dampers | 1 | 0 | 29-May-14 A | 08-Jun-14 A | |
| L16-8221 | HVAC Risers Duct Insulation | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| PH-8712 | PH - Complete Framing and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |

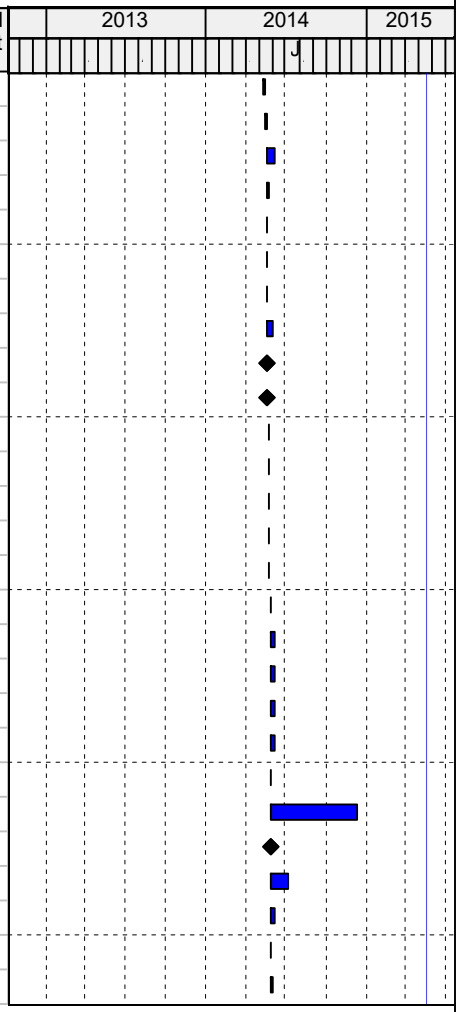


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-8714 | Stage PH/L18 roofing materials | 2 | 0 | 30-May-14 A | 30-May-14 A | |
| L08-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L08-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 02-Jun-14 A | 20-Jun-14 A | |
| PH-8704I | Correct support steel embeds | 2 | 0 | 02-Jun-14 A | 11-Jun-14 A | |
| L14-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 03-Jun-14 A | 04-Jun-14 A | |
| L17-8221 | HVAC Risers Duct Insulation | 1 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| PC-4010 | PC - Fireproof Entry Roof Steel | 5 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| I-4100 | Owner resolve trap primers issue (RFI 560) | 5 | 0 | 03-Jun-14 A | 20-Jun-14 A | |
| RF-6028 | Tower Roof - Structural Steel | 5 | 0 | 04-Jun-14 A | 17-Jun-14 A | |
| L14-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L1B-6005 | Head of Wall Fire Caulk at CMU (including East Servic | 2 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| ASI36r1 | ASI No. 36 (Revised) - MDP's Revision to E002 | 0 | 0 | 05-Jun-14 A | | |
| L14-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L15-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L16-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| ASI39 | ASI No. 39 - MDP's Electrical Revisions Rev. 17 | 0 | 0 | 09-Jun-14 A | | |
| I-2326 | RFI 233/ Install dampers | 1 | 0 | 09-Jun-14 A | 09-Jun-14 A | |
| I-2328 | RFI 233/ Install dampers | 1 | 0 | 09-Jun-14 A | 09-Jun-14 A | |
| I-2330 | RFI 233/ Install dampers | 1 | 0 | 10-Jun-14 A | 10-Jun-14 A | |
| L09-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 11-Jun-14 A | 12-Jun-14 A | |
| ASI25r2 | ASI No. 25 (Revised) - JBA's Interior Elevation Revisic | 0 | 0 | 11-Jun-14 A | | |
| ASI29r3 | ASI No. 29 (Revised) - JBA's Interior Elevation Revs a | 0 | 0 | 11-Jun-14 A | | |
| ASI35r1 | ASI No. 35 (Revised) - JBA's Interior Design Revisions | 0 | 0 | 11-Jun-14 A | | |

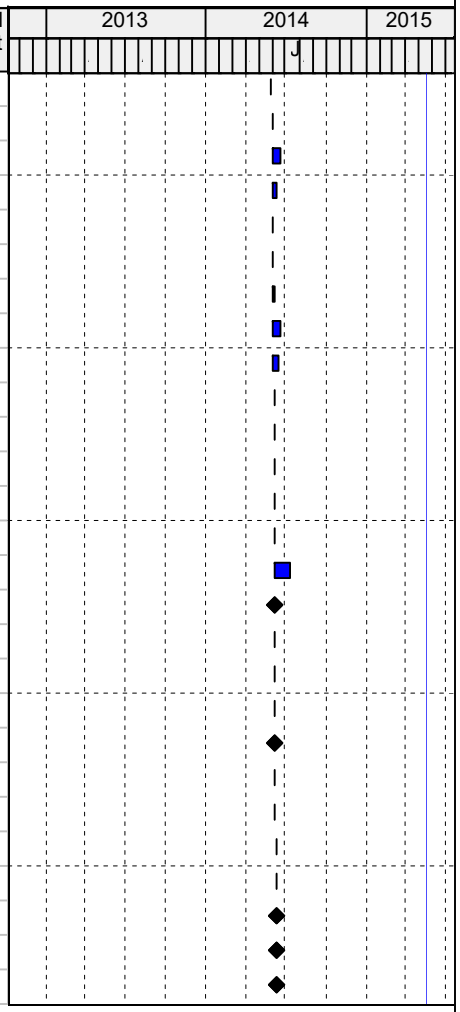


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-2332 | RFI 233/ Install dampers | 1 | 0 | 11-Jun-14 A | 12-Jun-14 A | |
| I-5018 | RFI 566 - Street Overlay Pavement Marking Reqs | 1 | 0 | 11-Jun-14 A | 01-Jul-14 A | |
| I-2970 | RFI 567 Grease Duct Conflict with Mens Restroom (P | 1 | 0 | 12-Jun-14 A | 01-Aug-14 A | |
| I-2336 | RFI 233/ Install dampers | 1 | 0 | 13-Jun-14 A | 16-Jun-14 A | |
| I-2334 | RFI 233/ Install dampers | 1 | 0 | 17-Jun-14 A | 18-Jun-14 A | |
| I-3702 | Complete wall framing at Stair/Elevator 5 (LL4) | 2 | 0 | 18-Jun-14 A | 20-Jun-14 A | |
| I-3720 | Fireproof added steel between Stair 1 and Elevator 5 | 5 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| I-3722 | Complete GWB between Stair 1 and Elevator 5 shaft | 10 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| ASI40 | ASI No. 40 - MDP's Electrical Revisions Rev. 18 | 0 | 0 | 18-Jun-14 A | | |
| LL1-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 22-Jul-14 A | |
| TC-5912 | Tower Crane pour-backs (LL4 to L3) | 4 | 0 | 19-Jun-14 A | 26-Jun-14 A | |
| LL1-Z2-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| I-2338 | RFI 233/ Install dampers | 1 | 0 | 19-Jun-14 A | 23-Jun-14 A | |
| LL4-6005 | LL4 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| LL3-6005 | LL3 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| L03-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 21-Jun-14 A | 21-Jun-14 A | |
| L06-6040 | Test Heat Pumps - L3, L4, L5 and L6 | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L03-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| L17-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL2-6005 | LL2 - Seismic Head Of Wall Fire Caulk at CMU | 5 | 0 | 24-Jun-14 A | 18-Jul-14 A | |
| I-3704 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL1-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z2-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z3-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 04-Aug-14 A | |
| L1L-6005 | Head of Wall Fire Caulk at CMU (including back of ho | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1K-6005 | Head of Wall Fire Caulk at CMU & Inspection | 2 | 0 | 24-Jun-14 A | 08-Aug-14 A | |
| L03-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |

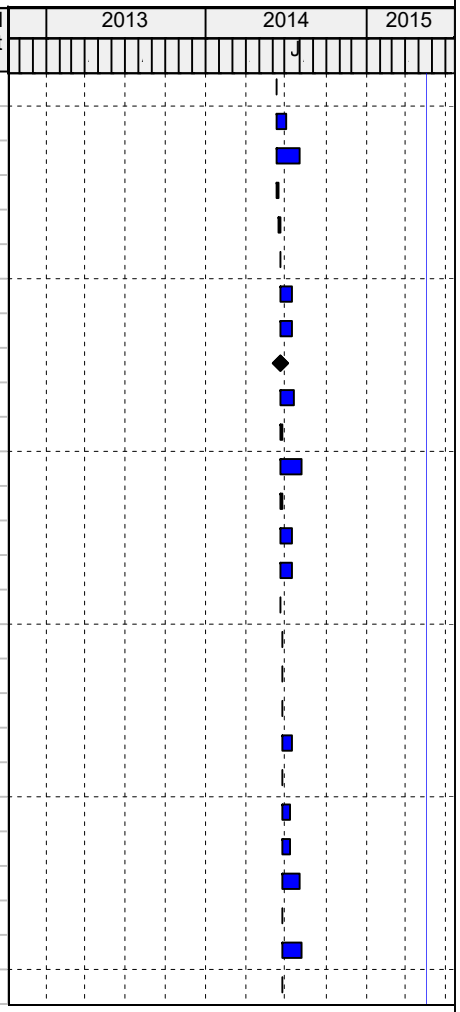



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| I-2340 | RFI 233/ Install dampers | 1 | 0 | 24-Jun-14 A | 26-Jun-14 A | |
| L17-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| I-3710 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| I-3712 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| L1K-6018a | Install Kitchen hoods and grease ducts (OFCI) | 10 | 0 | 25-Jun-14 A | 07-Oct-14 A | |
| L03-8604 | L3 Pool - Plumbing R/I | 5 | 0 | 25-Jun-14 A | 10-Nov-14 A | |
| ASI41 | ASI No. 41 - Kay Lang's Interior Design CD Set | 0 | 0 | 25-Jun-14 A | | |
| L04-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 26-Jun-14 A | 03-Jul-14 A | |
| L09-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 26-Jun-14 A | 26-Jun-14 A | |
| I-3706 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 26-Jun-14 A | 10-Jul-14 A | |
| L03-8600 | L3 Pool - Framing & HM frames | 5 | 0 | 26-Jun-14 A | 20-Nov-14 A | |
| L05-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L08-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L04-7018 | Electrical Rough-In | 1 | 0 | 27-Jun-14 A | 22-Jul-14 A | |
| L04-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 27-Jun-14 A | 23-Jul-14 A | |
| I-2342 | RFI 233/ Install dampers | 1 | 0 | 27-Jun-14 A | 28-Jun-14 A | |
| L03-7020 | HVAC Rough-In | 1 | 0 | 29-Jun-14 A | 15-Jul-14 A | |
| L1RR-8100 | Insulation [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8100 | Insulation [DELETED - included in Ballroom activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8100 | Insulation [DELETED - included in Meeting Rooms ac | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8102 | GWB Hang [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8215 | GWB Tape [DELETED - included in Meeting Rooms a | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8104 | Prime Paint [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |

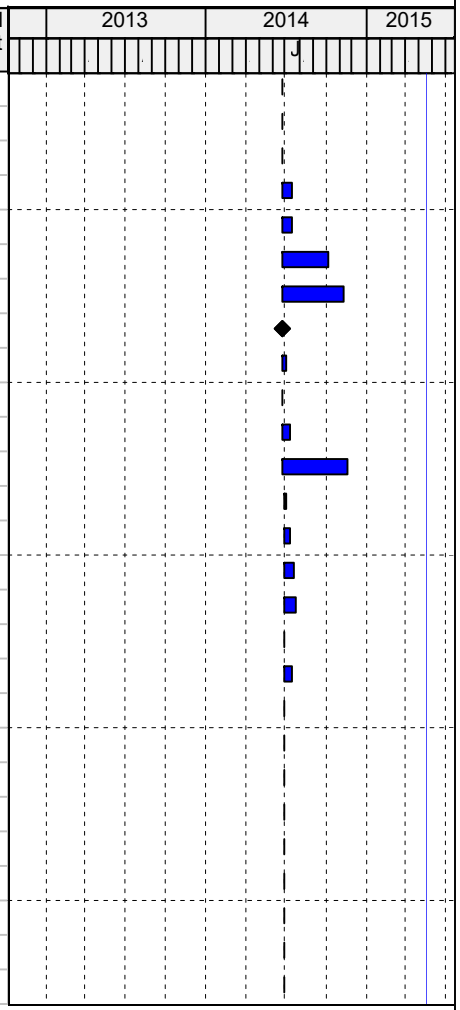


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z6-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8102 | GWB Hang [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8215 | GWB Tape [DELETED - included in Ballroom activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8104 | Prime Paint [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8102 | GWB Hang [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8215 | GWB Tape [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8104 | Prime Paint [DELETED - included in Kitchen activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L03-7018 | Electrical Rough-In | 1 | 0 | 01-Jul-14 A | 14-Jul-14 A | |
| L03-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Jul-14 A | 15-Jul-14 A | |
| I-5020 | RFI 583 - Tree Grate Location | 1 | 0 | 01-Jul-14 A | 23-Jul-14 A | |
| I-5022 | RFI 585 - Porte Cochere Concrete Bench & Planters | 1 | 0 | 01-Jul-14 A | 09-Jul-14 A | |
| I-5024 | RFI 586 - Bench Support at Porte Cochere (related to | 1 | 0 | 01-Jul-14 A | 09-Jul-14 A | |
| L10-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7102 | Install Vertical Heat Pump | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L03-7116 | Frame Walls | 1 | 0 | 02-Jul-14 A | 14-Jul-14 A | |
| L03-7118 | Install HM Door Frame | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L04-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L05-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L07-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L08-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L09-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |

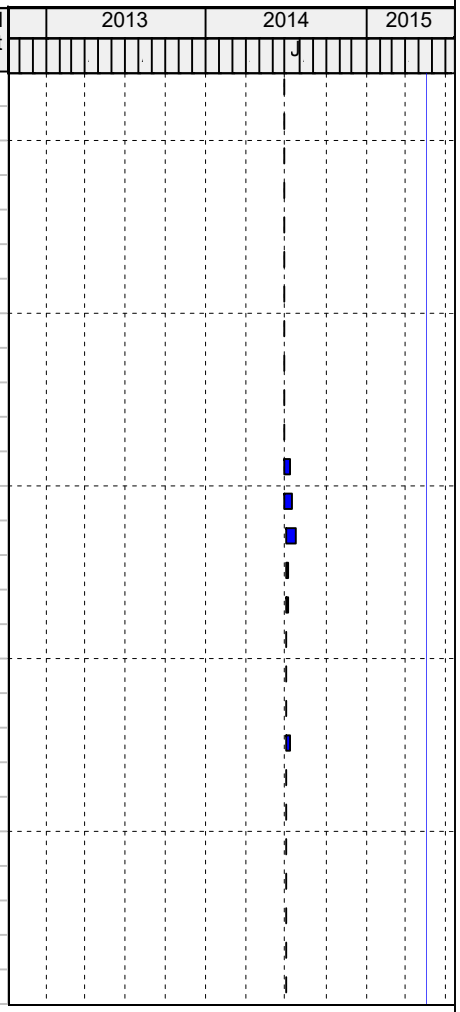



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L12-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| I-3906 | Ballroom Parapet Height Issue/ frame parapet | 1 | 0 | 02-Jul-14 A | 21-Jul-14 A | |
| L06-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| I-3708 | Complete wall framing at Stair/Elevator 5 (LL3) | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L11-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 03-Jul-14 A | 07-Jul-14 A | |
| L04-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L05-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L06-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L07-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L08-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L17-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L10-6040 | Test Heat Pumps - L7, L8, L9 and L10 | 3 | 0 | 07-Jul-14 A | 09-Jul-14 A | |
| L10-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L03-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |

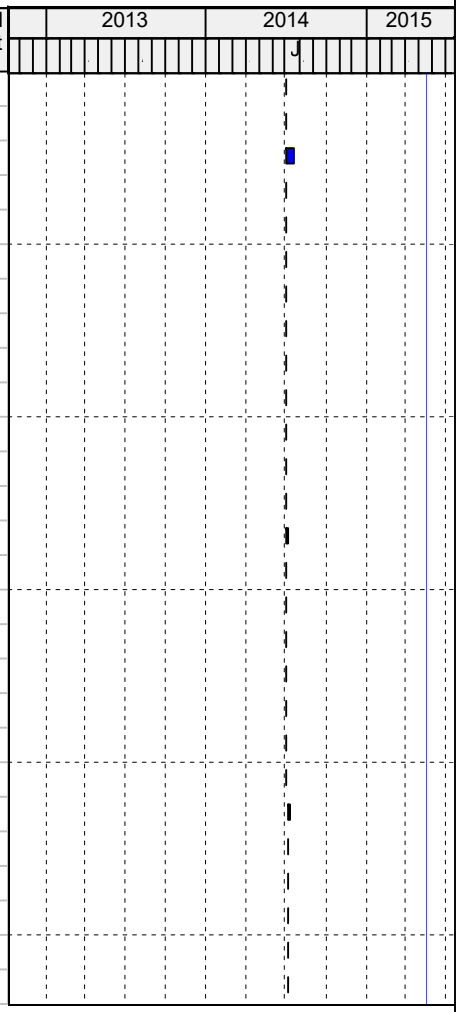



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L04-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L05-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L06-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L07-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L08-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L09-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L10-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L12-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L14-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L11-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Jul-14 A | 29-Jul-14 A | |
| L03-8602 | L3 Pool - Fire Sprinkler R/I | 5 | 0 | 08-Jul-14 A | 22-Jul-14 A | |
| L03-7016 | Install HM door frame | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L11-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L16-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 09-Jul-14 A | |
| L04-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |

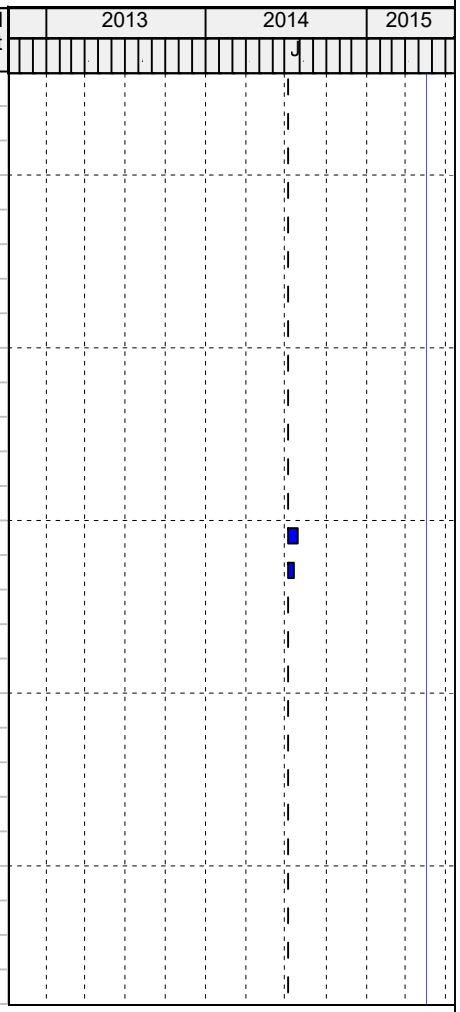



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L12-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| MP-FAB1 | Fabricate and Deliver Bronze Gold Horizontal Panels | 30 | 0 | 09-Jul-14 A | 15-Jul-14 A | |
| L04-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L05-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L06-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L16-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| MP-FAB2 | Fabricate and Deliver Silver Vertical Panels | 45 | 0 | 10-Jul-14 A | 25-Aug-14 A | |
| ASI27capt | ASI No. 27 - City Approved ASI No. 27 (Tower Plumbi | 0 | 0 | 10-Jul-14 A | | |

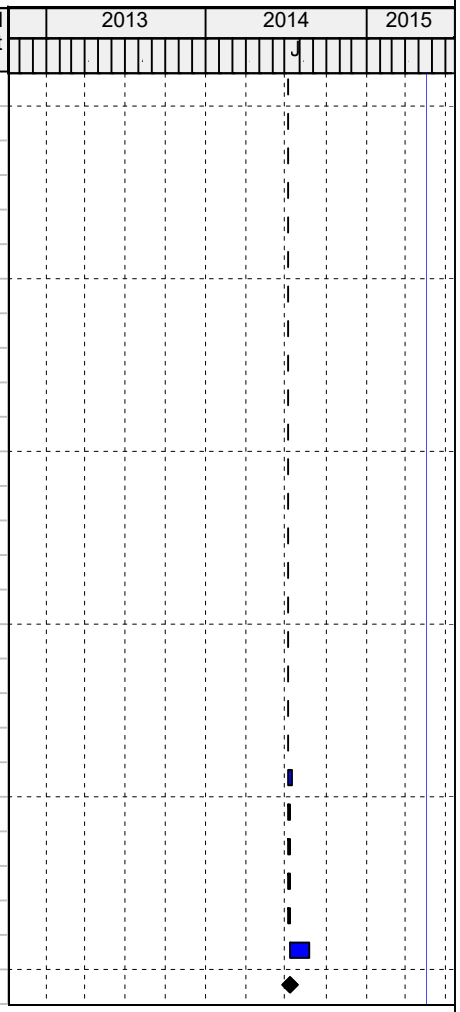



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ASI27cam | ASI No. 27 - City Approved ASI No. 27 (Mechanical) | 0 | 0 | 10-Jul-14 A | | |
| ASI36ca | ASI No. 36 - MDP Electrical Revisions Rev. 16 (City Ap | 0 | 0 | 10-Jul-14 A | | |
| ASI38ca | ASI No. 38 - MDP's Bar & Concierge Plumbing Revisi | 0 | 0 | 10-Jul-14 A | | |
| I-5026 | RFI 611 - Landscaping at Porte Cochere Planters | 1 | 0 | 10-Jul-14 A | 18-Jul-14 A | |
| I-3004 | ASI 38/ Issue ASI 38 | 0 | 0 | 11-Jul-14 A | | |
| I-3006 | ASI 38/ Release bar area for x-ray examination | 5 | 0 | 11-Jul-14 A | 03-Sep-14 A | |
| L07-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| LL1-Z2-6018a | Complete Mech RI at tower crane opening (LL1) | 4 | 0 | 14-Jul-14 A | 17-Jul-14 A | |
| L08-6223 | Frame Corridor Ceilings | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| SW-2006a | Complete Dry Utilities (Phase 2) | 5 | 0 | 14-Jul-14 A | 24-Jul-14 A | |
| L04-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L04-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L05-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L06-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L04-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |

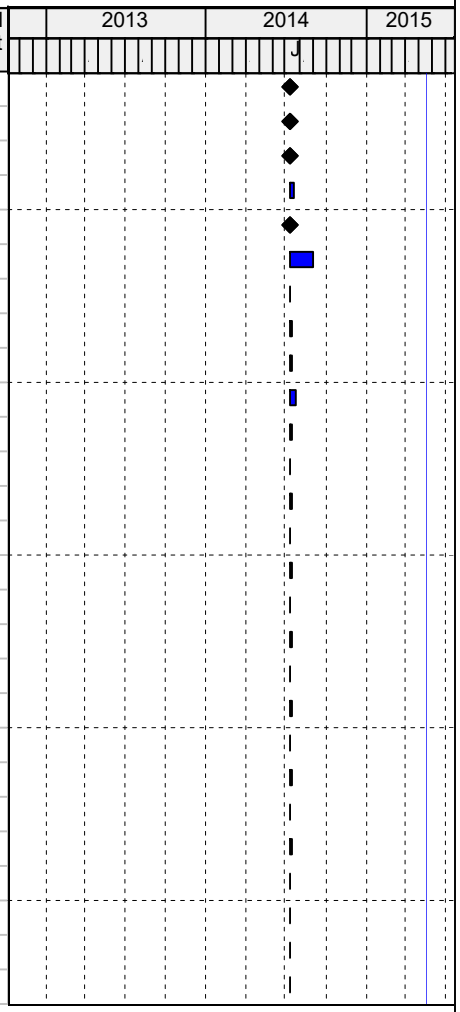



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L11-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L11-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L12-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L12-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L15-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L15-7102 | Install Vertical Heat Pump | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L1B-6026 | Install operable partition steel | 2 | 0 | 15-Jul-14 A | 08-Aug-14 A | |
| L09-6223 | Frame corridor ceilings | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L03-7120 | Electrical Rough-In | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L07-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L07-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L08-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L08-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L09-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L09-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L03-7142 | Install Laundry Chute (All Levels) | 9 | 0 | 15-Jul-14 A | 25-Jul-14 A | |
| LL2-2045 | LL2 - Electrical Room build-out | 15 | 0 | 15-Jul-14 A | 26-Sep-14 A | |
| L03-7122 | HVAC Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L03-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |

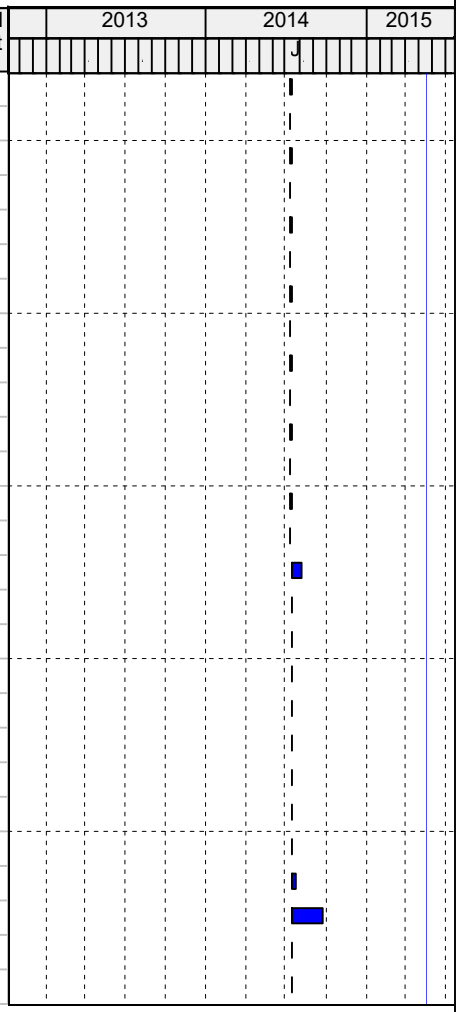



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L05-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L06-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L07-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L07-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L08-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L08-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L09-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L09-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L11-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L11-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L12-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L12-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L15-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L15-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L16-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |

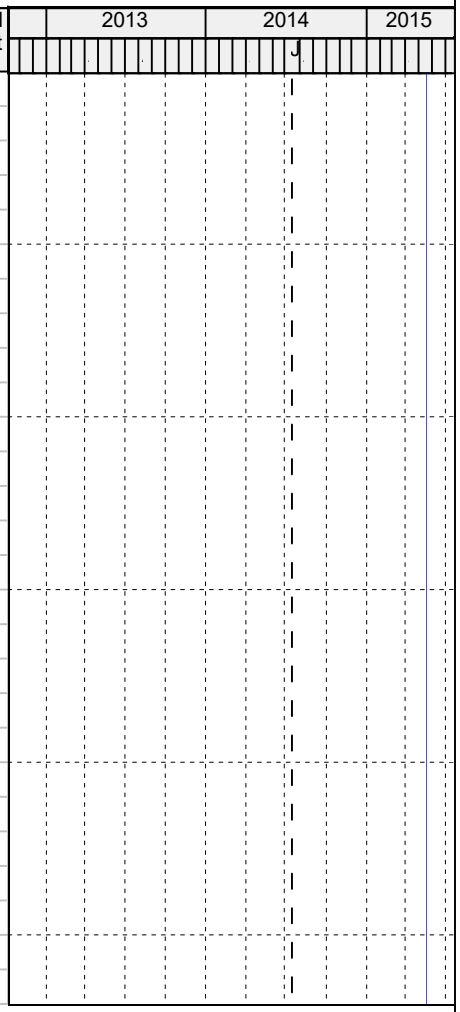



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L17-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| ASI41r1 | ASI No. 41 (Revised) - Kay Lang's Interior Design CD | 0 | 0 | 16-Jul-14 A | | |
| ASI43 | ASI No. 43 - MDP's Electrical Revisions Rev. 19 | 0 | 0 | 16-Jul-14 A | | |
| L03-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L04-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L04-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L05-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L05-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L06-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L06-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L07-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L08-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L09-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L11-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |

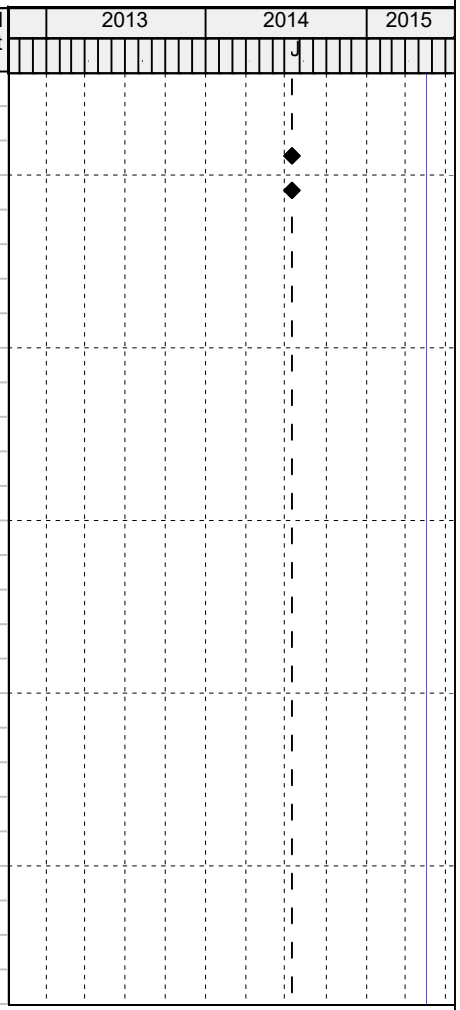



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L12-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L12-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L16-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| ASI42 | ASI No. 42 - JBA's Arch Revs to Lobby and Concierge | 0 | 0 | 17-Jul-14 A | | |
| ASI45 | ASI No. 45 - JBA's Revised Guestroom Suite Layouts | 0 | 0 | 17-Jul-14 A | | |
| L03-8608 | L3 Pool - Electrical R/I | 5 | 0 | 18-Jul-14 A | 10-Nov-14 A | |
| L03-8610 | L3 Pool - Fire Alarm / Elec Specialties R/I | 5 | 0 | 18-Jul-14 A | 10-Nov-14 A | |
| L15-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L15-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| L17-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L17-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| LL2-2052 | LL2 - Install fuel piping and exhaust duct to Generatc | 8 | 0 | 21-Jul-14 A | 15-Aug-14 A | |
| L04-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L04-7016 | Install HM door frame | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L07-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L08-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L10-7116 | Frame Walls | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L16-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 21-Jul-14 A | 22-Jul-14 A | |
| L16-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L17-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| ASI41r2 | ASI No. 41 (Revised) - Kay Lang's Interior Design Spe | 0 | 0 | 22-Jul-14 A | | |
| ASI44 | ASI No. 44 - MDP's Mechanical Revisions Rev. 17 | 0 | 0 | 24-Jul-14 A | | |
| MPT-1002 | Tower - Install Elevation 35 (east elevation-south half) | 8 | 0 | 25-Jul-14 A | 04-Aug-14 A | |
| L16-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 25-Jul-14 A | 25-Jul-14 A | |
| L11-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |

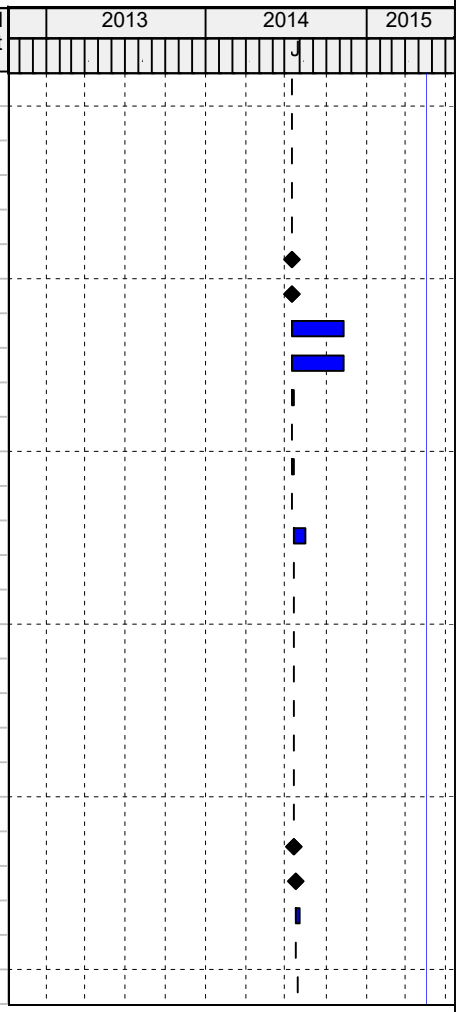


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L14-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L15-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L16-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L10-6223 | Frame Corridor Ceilings | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L11-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L15-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L15-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L11-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L14-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L16-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| I-1304 | Prep Kitchen - Additional framing (ASI 30) | 2 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-2302 | Framing "Go Back" work at LL1 for RFI 233 | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| I-2502 | Electrical rework at LL1 for ASIs 7, 9r2, 14, 27 | 4 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| L12-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L1B-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 01-Aug-14 A | 15-Aug-14 A | |
| MPL4-1000 | Upper L4 Ballroom - Install Elevations 1, 2 & 3 (south | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1000 | Tower - Install Elevations 26-27 (west elevation) [DEL | 13 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPP-1002 | Podium - Install Elevations 1 & 2 (west elevation, sou | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPP-1008 | Podium - Install Elevations 7 & 8 (north & east elevati | 9 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1002 | Upper L4 Ballroom - Install Elevation 10 (west elevatio | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1004 | Upper L4 Ballroom - Install Elevation 9 (north elevatio | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |

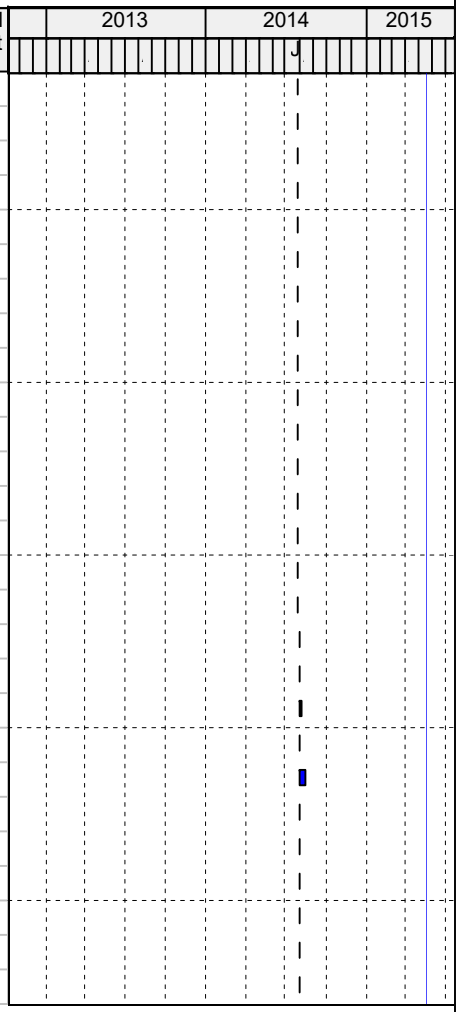


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPT-1006 | Tower - Install Elevation 40 (east return-east end) [DE | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1010 | Tower - Install Elevations 51 (north elevation) [DELET | 8 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-4004 | East Stitched - Install metal panels [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L11-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L11-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L15-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L14-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L17-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| MPT-1010b | Tower - Install Elevation 45 [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| ASI46 | ASI No. 46 - Concept Services Revised Kitchen Drawi | 0 | 0 | 01-Aug-14 A | | |
| L16-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 04-Aug-14 A | 05-Aug-14 A | |
| L11-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Aug-14 A | 08-Aug-14 A | |
| L04-7020 | HVAC Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |

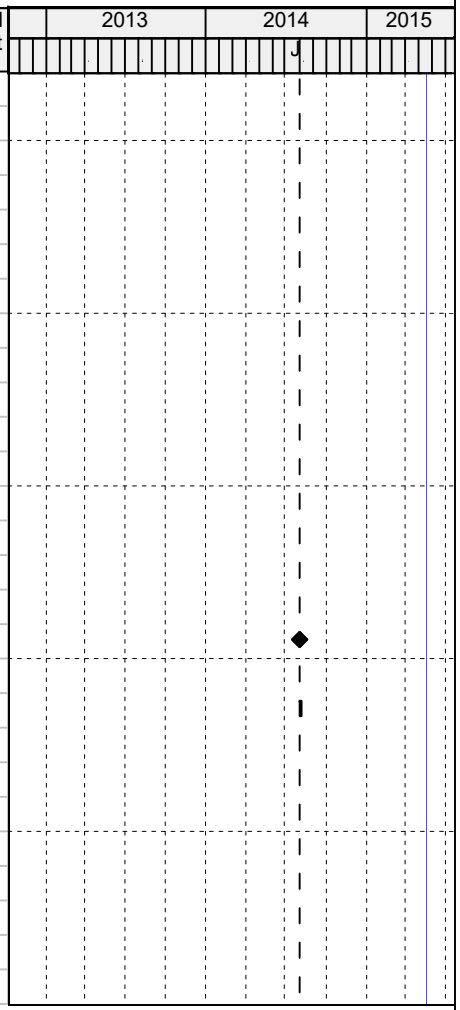



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L14-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L15-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 05-Aug-14 A | 07-Aug-14 A | |
| L05-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L06-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L07-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L08-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L09-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L10-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7018 | Electrical Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L14-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 05-Aug-14 A | 06-Aug-14 A | |
| L14-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| I-4104 | Install added trap primers - LL1 | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L06-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L07-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L08-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L09-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L10-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7020 | HVAC Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |

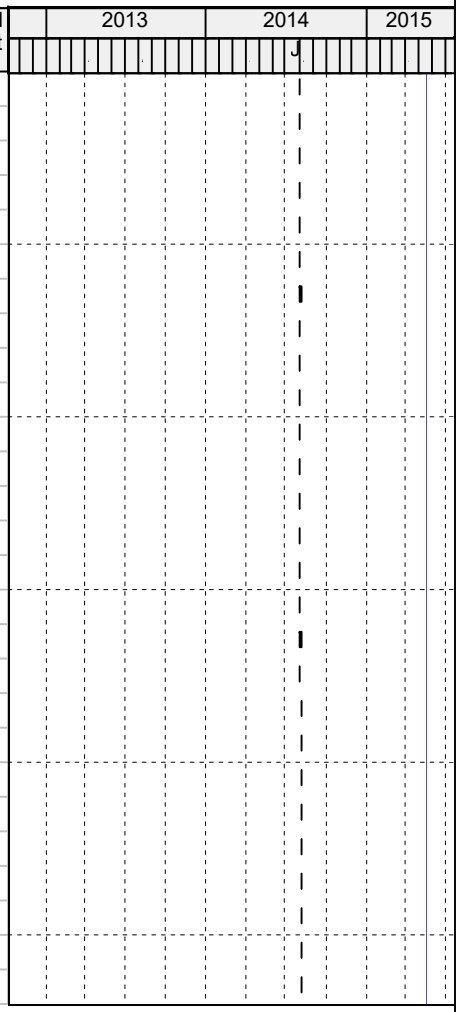



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L16-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| EL-1220 | Elevator fronts delivered | 0 | 0 | 07-Aug-14 A | | |
| L12-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L12-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-6223 | Frame Corridor Ceilings | 4 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L11-7016 | Install HM door frame | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L12-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L15-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L15-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L16-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L16-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L17-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L17-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| ASI48 | ASI No. 48 - MDP Revisions to Electrical & Plumbing | 0 | 0 | 08-Aug-14 A | | |
| L14-6040 | Test Heat Pumps - L11, L12 and L14 | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| PH-6026 | PH - Insulation/Vapor Barrier/GWB at Exterior Walls | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| L11-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L11-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |

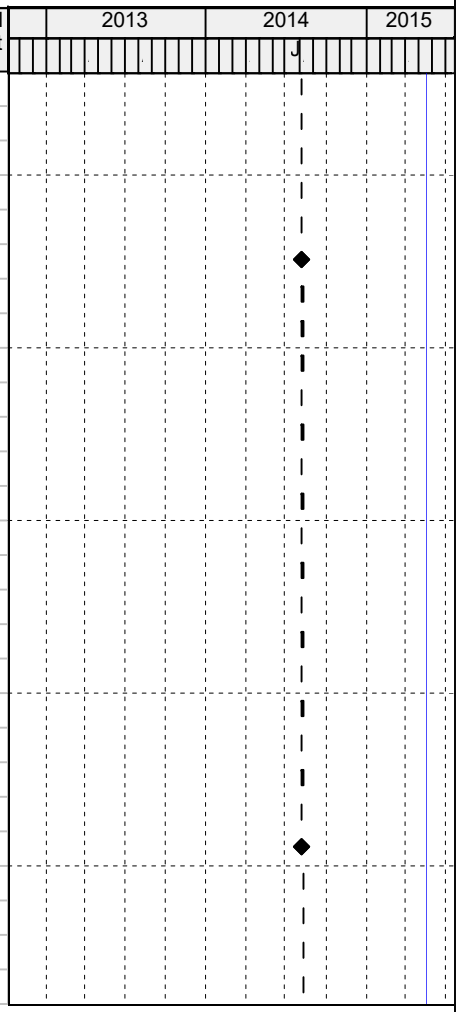



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7026 | Inspections for GWB Cover | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 13-Aug-14 A | 13-Aug-14 A | |
| L15-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 14-Aug-14 A | 15-Aug-14 A | |
| LL2E-8108 | LL2 - Set fire pumps and equipment | 5 | 0 | 14-Aug-14 A | 29-Sep-14 A | |
| L10-7028 | GWB Hang/Tape/Finish | 5 | 0 | 14-Aug-14 A | 05-Dec-14 A | |
| L12-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L12-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L16-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L1BOH2-6008 | Int Wall Framing & Inspection | 5 | 0 | 14-Aug-14 A | 20-Aug-14 A | |
| I-4106 | Install added trap primers - L1 | 1 | 0 | 15-Aug-14 A | 15-Aug-14 A | |
| L14-6223 | Frame Corridor Ceilings | 4 | 0 | 15-Aug-14 A | 16-Aug-14 A | |
| L03-8136 | Install Counter Subtops | 3 | 0 | 15-Aug-14 A | 18-Aug-14 A | |
| LL2-2054 | LL2 - GWB, Hang 1st Layer at Laundry Room | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| LL2E-8112 | LL2 - Form/Pour Fire Pump Pads/Curbs | 2 | 0 | 16-Aug-14 A | 18-Aug-14 A | |
| LL1-6014Ia | L1 bar redesign - rework plumbing at ceilings | 10 | 0 | 18-Aug-14 A | 05-Jan-15 A | |
| L15-6223 | Frame Corridor Ceilings | 4 | 0 | 18-Aug-14 A | 21-Aug-14 A | |
| L17-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |

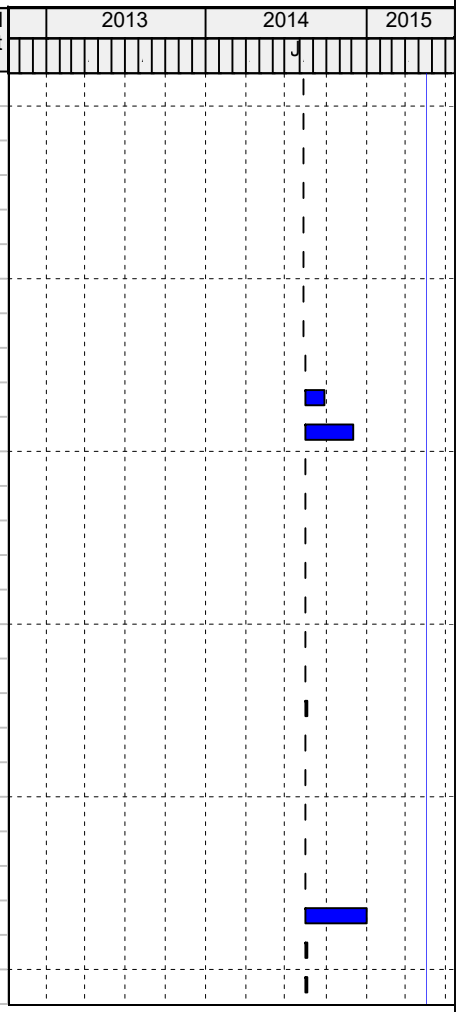



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Aug-14 A | 18-Aug-14 A | |
| L04-8136 | Install Counter Subtops | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-6014Ic | L1 bar redesign - rework electrical at ceilings | 10 | 0 | 18-Aug-14 A | 05-Jan-15 A | |
| LL2E-8114 | LL2 - Set Tube Steel at Door | 1 | 0 | 19-Aug-14 A | 19-Aug-14 A | |
| L17-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 20-Aug-14 A | 21-Aug-14 A | |
| L17-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 20-Aug-14 A | 20-Aug-14 A | |
| L05-8136 | Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 26-Aug-14 A | |
| L06-8136 | Bathrooms - Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 13-Oct-14 A | |
| L16-6223 | Frame Corridor Ceilings | 4 | 0 | 21-Aug-14 A | 29-Aug-14 A | |
| L17-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 21-Aug-14 A | 22-Aug-14 A | |
| L17-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 21-Aug-14 A | 21-Aug-14 A | |
| L1BOH2-6016 | Electrical RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6018 | HVAC RI | 4 | 0 | 21-Aug-14 A | 17-Oct-14 A | |
| L15-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7020 | HVAC Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7022 | Fire Sprinkler Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| LL2E-8116 | LL2 - Set Door Jamb | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| ASI49 | ASI No. 49 - SCA Transformer Vault Alcove Connectic | 0 | 0 | 22-Aug-14 A | | |
| L03-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L04-7028 | GWB Hang/Tape/Finish | 5 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L05-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L05-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L06-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L06-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |

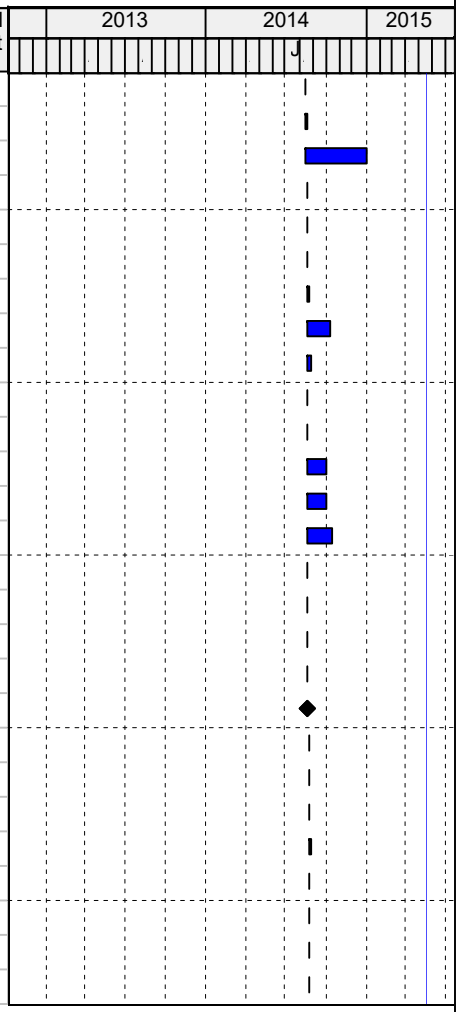



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L03-8123 | Bathroom "Barn Doors" On Site | 0 | 0 | 25-Aug-14 A | | |
| LL3-6026 | LL3 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL2-6026 | LL2 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL1-Z3-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L1BOH2-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L02-6026 | L2 - Set Elevator Fronts (Cars 1-4 | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |

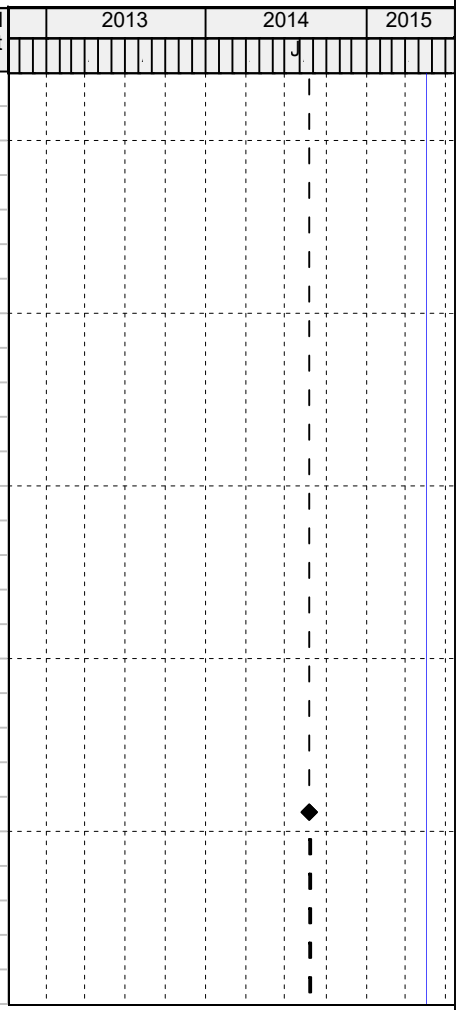



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L04-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L05-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L06-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L07-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L08-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L09-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L10-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L11-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L12-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L14-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L15-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L16-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L17-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| MPT-1008 | Tower - Install E/W Wing, N. Side West Half (Elev 50,: | 7 | 0 | 26-Aug-14 A | 03-Oct-14 A | |
| L06-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L07-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L08-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L05-7026 | Inspections for GWB Cover | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L05-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L11-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 08-Dec-14 A | |
| L12-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L14-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L03-8105a | Painting - Split Door Jambs | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L09-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L10-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L11-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |

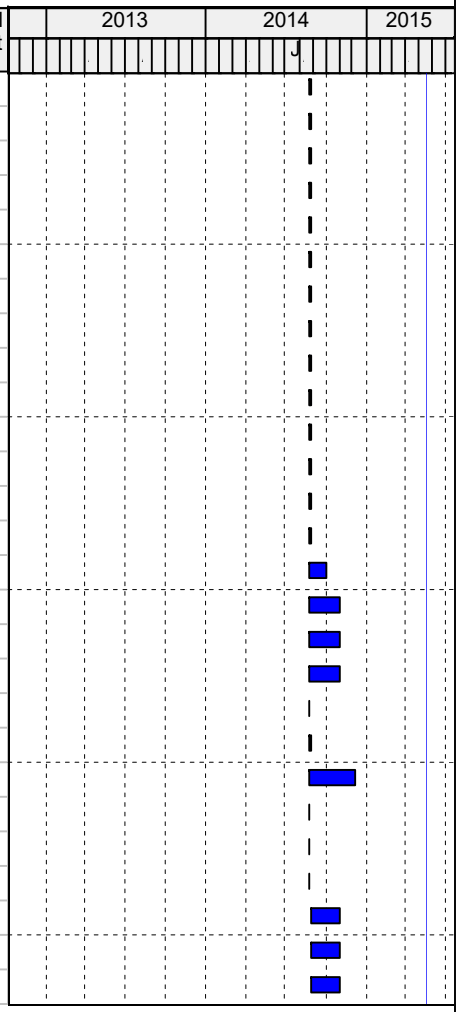



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L14-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L15-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L16-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L05-8201 | Install ACT Grid @ Corridors | 2 | 0 | 27-Aug-14 A | 28-Aug-14 A | |
| L16-7022 | Fire Sprinkler Rough-In | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L04-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L06-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| EP-5110a | L1 - Install Steel at Revolving Door Opening | 3 | 0 | 27-Aug-14 A | 29-Aug-14 A | |
| L05-8105a | Painting - Split Door Jambs | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| ASI50 | ASI No. 50 - Updated S1 Plumbing Fixture | 0 | 0 | 28-Aug-14 A | | |
| I-4102 | Install added trap primers - LL2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4108 | Install added trap primers - L2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4110 | Install added trap primers - L3 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4112 | Install added trap primers - Roof PH | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| L03-8124d | Flooring On Site and Acclimated | 2 | 0 | 29-Aug-14 A | 01-Sep-14 A | |
| ASI47 | ASI No. 47 - Architectural and Interior Design Revisior | 0 | 0 | 29-Aug-14 A | | |
| L02-5102 | L2 - Storefront Frames | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| L04-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L05-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L17-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L03-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L12-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L14-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L07-8136 | Install Counter Subtops | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| LL1-Z3-FCC10 | FCC - Set Jamb | 1 | 0 | 02-Sep-14 A | 03-Sep-14 A | |
| MPT-1004 | Tower - Install E/W Wing, S. Side w/o Windows (Elev | 10 | 0 | 03-Sep-14 A | 17-Oct-14 A | |

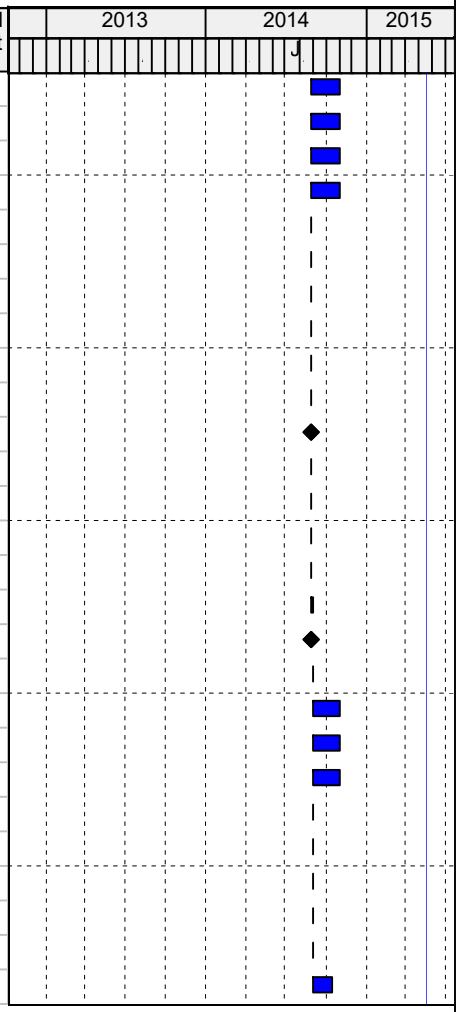



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-7028 | GWB Hang/Tape/Finish | 5 | 0 | 03-Sep-14 A | 02-Dec-14 A | |
| L12-7028 | GWB Hang/Tape/Finish | 5 | 0 | 03-Sep-14 A | 08-Dec-14 A | |
| L03-8126a | Doors & Hardware On Site | 0 | 0 | 03-Sep-14 A | | |
| LL1-Z3-FCC12 | FCC - Sheetrock Outside Wall | 1 | 0 | 03-Sep-14 A | 03-Sep-14 A | |
| ASI46r1 | ASI No. 46 (Revised) - Revised Kitchen Equipment M | 0 | 0 | 03-Sep-14 A | | |
| L16-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| L17-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Sep-14 A | 11-Sep-14 A | |
| L02-5104b | L2 - Install Storefront Temporary Enclosures | 1 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| LL1-Z3-FCC14 | FCC - Verify Fire Caulk OK & Inspect Room OK to 2n | 1 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| I-3008 | ASI 38/ Coordinate and perform x-ray examination | 7 | 0 | 04-Sep-14 A | 24-Sep-14 A | |
| L02-5104a | L2 - Measure/Fabricate Storefront Glazing | 15 | 0 | 05-Sep-14 A | 18-Sep-14 A | |
| LL1-Z3-FCC16 | FCC - GWB, Hang 2nd Layer | 2 | 0 | 05-Sep-14 A | 08-Sep-14 A | |
| ASI52 | ASI No. 52 - MDP Electrical Revisions Rev. 21 | 0 | 0 | 05-Sep-14 A | | |
| I-5028 | RFI 687 - Planter at Porte Cochere Grid V & 25 | 1 | 0 | 05-Sep-14 A | 10-Sep-14 A | |
| L03-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L15-7018 | Electrical Rough-In | 1 | 0 | 08-Sep-14 A | 08-Sep-14 A | |
| EL-1228 | Construct/Approve elevator lobby framing mockup (L | 3 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| LL2E-8118 | LL2 - Frame Infill, Install Densglass & Inspect at Fire I | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L06-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L08-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L15-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7018 | Electrical Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L3-5104a | L3 - Measure/Fabricate Storefront Glazing | 15 | 0 | 09-Sep-14 A | 30-Sep-14 A | |
| L03-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 23-Sep-14 A | |

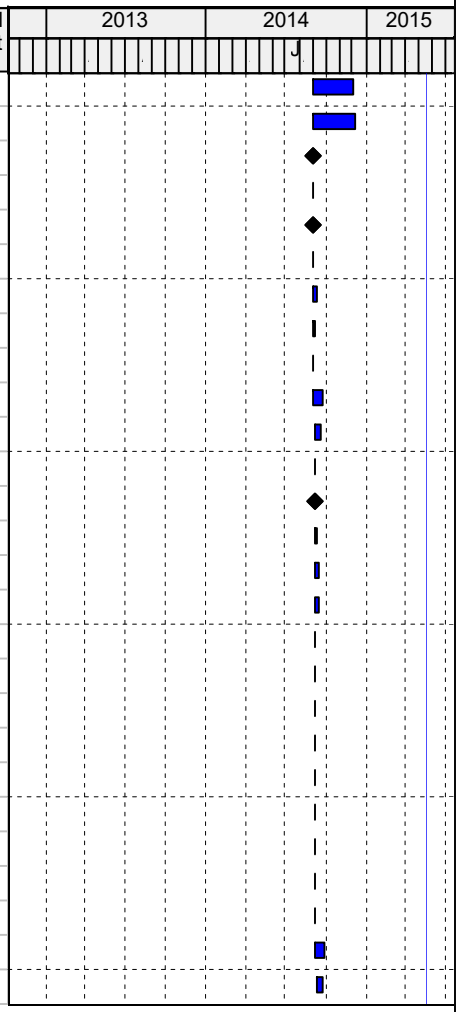



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L04-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L06-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| L08-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| L05-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L06-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L06-7028 | GWB Hang/Tape/Finish | 5 | 0 | 10-Sep-14 A | 02-Dec-14 A | |
| L08-7028 | GWB Hang/Tape/Finish | 5 | 0 | 10-Sep-14 A | 05-Dec-14 A | |
| L15-7026 | Inspections for GWB Cover | 1 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| LL2E-8120 | LL2 - Insulation, Vapor Barrier & Inspect at Fire Pump | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| ASI53 | ASI No. 53 - Pool Chemical Storage System | 0 | 0 | 10-Sep-14 A | | |
| L08-8395 | Framing at Elevator Lobby | 4 | 0 | 11-Sep-14 A | 17-Sep-14 A | |
| L15-7028 | GWB Hang/Tape/Finish | 5 | 0 | 11-Sep-14 A | 08-Dec-14 A | |
| L08-8136 | Install Counter Subtops | 3 | 0 | 11-Sep-14 A | 16-Sep-14 A | |
| L02-6025 | L2 - Framing Go-Back Work (left out for mechanical e | 4 | 0 | 11-Sep-14 A | 02-Oct-14 A | |
| L1-5104a | L1 - Measure/Fabricate Storefront Glazing | 15 | 0 | 12-Sep-14 A | 18-Sep-14 A | |
| L1B-8102c | Finish framing and MEP at Main Ballroom East Wall ( | 10 | 0 | 12-Sep-14 A | 02-Oct-14 A | |
| L09-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L10-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L11-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L12-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L16-7026 | Inspections for GWB Cover | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| MPT-1014 | Tower - Install E/W Wing, N. Side, E. Half (Elev 46-49 | 8 | 0 | 15-Sep-14 A | 28-Oct-14 A | |
| LL2-6032 | LL2 - Complete Framing (Including Elevator Lobby) | 4 | 0 | 15-Sep-14 A | 18-Sep-14 A | |
| L1-5104b | L1 - Install Storefront Temporary Enclosures | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| LL1-Z3-FCC18 | FCC - Install Temp Door | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |

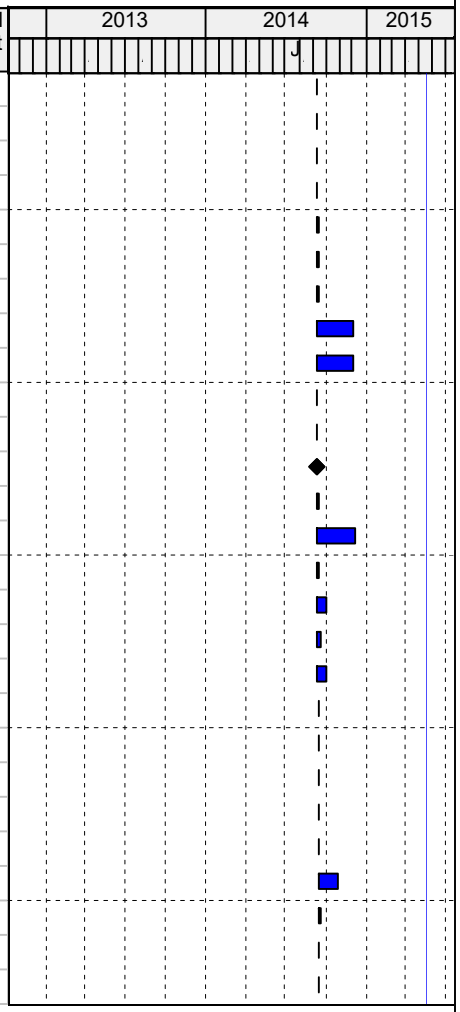



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2058a | LL2 - GWB Hang 1st Layer | 5 | 0 | 15-Sep-14 A | 19-Sep-14 A | |
| LL2-2064 | LL2 - Generator Room - Finish Exhaust Piping | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| I-3010 | ASI 38/ Prepare proposal for MEP relocations | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| ASI51 | ASI No. 51 - Interior Design Revisions | 0 | 0 | 15-Sep-14 A | | |
| L16-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L07-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L09-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L10-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L14-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L15-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L03-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| L16-7028 | GWB Hang/Tape/Finish | 5 | 0 | 16-Sep-14 A | 08-Dec-14 A | |
| L17-7018 | Electrical Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L09-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L10-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| LL3-6028 | LL3 - Frame Elevator Lobby | 2 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| LL4-6026 | LL4 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| I-3012 | ASI 38/ Owner approve proposal for MEP relocations | 3 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| ASI50r1 | ASI No. 50 (Revised) - Updated Plumbing Fixtgure K' | 0 | 0 | 16-Sep-14 A | | |
| L11-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L12-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L14-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L15-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L04-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L17-7026 | Inspections for GWB Cover | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L17-7116 | Frame Walls | 4 | 0 | 17-Sep-14 A | 29-Sep-14 A | |

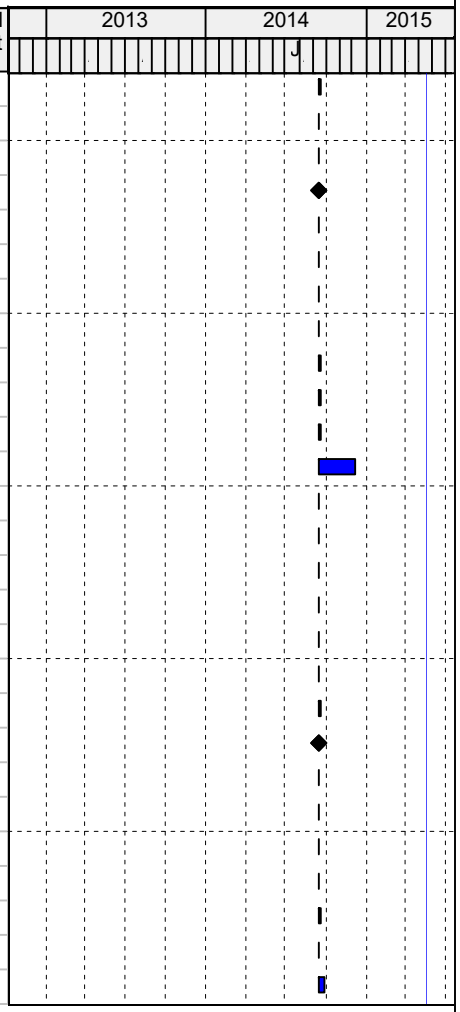



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2066 | LL2 - Generator Room - Finish Fuel Piping | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L16-8395 | Framing at Elevator Lobby | 4 | 0 | 18-Sep-14 A | 26-Sep-14 A | |
| L02-5104 | L2 - Storefront Glazing | 2 | 0 | 18-Sep-14 A | 22-Sep-14 A | |
| L17-7028 | GWB Hang/Tape/Finish | 5 | 0 | 18-Sep-14 A | 08-Dec-14 A | |
| LL4-6028 | LL4 - Frame Elevator Lobby | 2 | 0 | 18-Sep-14 A | 02-Oct-14 A | |
| MPT-1010a | Tower - Install E/W Wing, West End (Elev 52,53) | 8 | 0 | 18-Sep-14 A | 10-Oct-14 A | |
| ASI44ca | ASI No. 44 - MDP's Mechanical Revisions Rev. 17 (Ci | 0 | 0 | 18-Sep-14 A | | |
| LL2-2068 | LL2 - Generator Room - Electrical Finishes | 3 | 0 | 19-Sep-14 A | 30-Sep-14 A | |
| L07-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L09-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L04-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L05-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L03-8140 | Countertops On Site | 0 | 0 | 22-Sep-14 A | | |
| L03-8129a | Shower Doors On Site | 0 | 0 | 22-Sep-14 A | | |
| LL1-Z3-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L1BOH2-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2-2048a | LL2 - Move in Laundry Room Ironer | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2E-8122 | LL2 - Hang GWB at Fire Pump Room | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-FCC20 | FCC - Rough-In and Install Panels | 25 | 0 | 22-Sep-14 A | 21-Nov-14 A | |
| I-3014 | Core drill for MEP relocations | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L05-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L07-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 05-Dec-14 A | |
| L09-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 05-Dec-14 A | |
| L14-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 08-Dec-14 A | |
| L04-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L05-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L06-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |

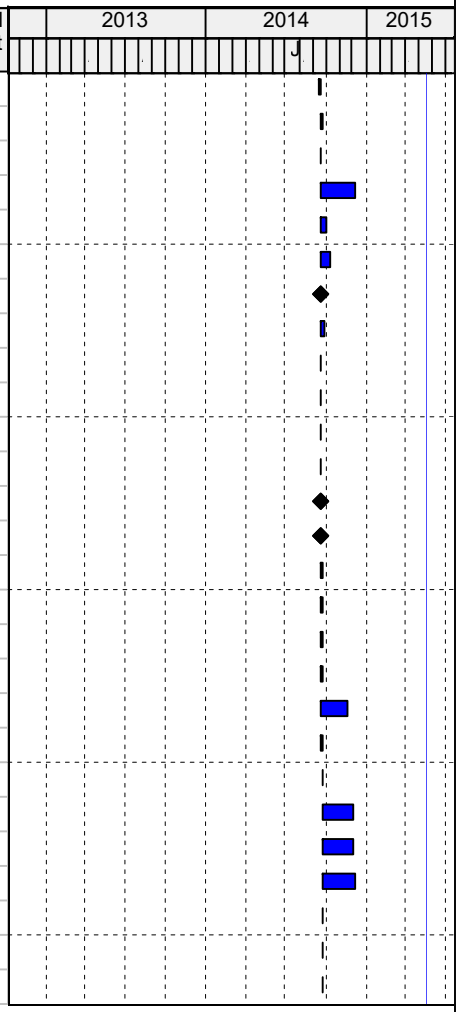



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| ASI53ca | ASI No. 53 - Pool Chemical Storage System (City Apr | 0 | 0 | 23-Sep-14 A | | |
| L04-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L06-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L04-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L05-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-7122 | HVAC Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| LL2-2058 | LL2 - Tape/Finish Laundry Room | 3 | 0 | 24-Sep-14 A | 26-Sep-14 A | |
| I-5034 | RFI 717 - Porte Cochere Paving Details | 1 | 0 | 24-Sep-14 A | 29-Oct-14 A | |
| L08-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L17-8395 | Framing at Elevator Lobby | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L05-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L06-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L07-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L08-7120 | Electrical Rough-In | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| LL2E-8124 | LL2 - Temp-In Louver Opening at Fire Pump Room | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L1-5104c | L1 - Install Storefront at Main Entry Facade | 5 | 0 | 25-Sep-14 A | 10-Oct-14 A | |
| I-5030 | RFI 715 - Additional Site Paving Per City | 1 | 0 | 25-Sep-14 A | 14-Oct-14 A | |
| L16-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L08-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |

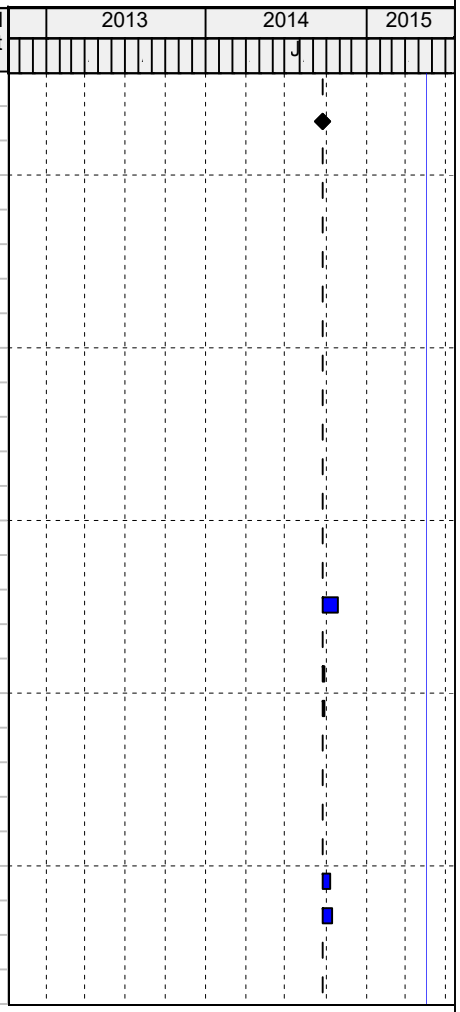



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L10-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L16-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L17-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L17-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L09-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L09-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L11-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L12-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L14-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L15-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L17-7118 | Install HM Door Frame | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| LL3-6030 | LL3 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL4-6030 | LL4 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL2-6034 | LL2 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L1BOH2-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L02-6030 | L2 - Framing at Elevator Lobby & North Half | 4 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| MPT-1022 | Tower - Caulking, west | 8 | 0 | 29-Sep-14 A | 03-Nov-14 A | |
| PH-6015 | PH - Set Boilers and Pumps | 12 | 0 | 29-Sep-14 A | 15-Oct-14 A | |
| L11-8204 | Bathrooms - Vinyl Wall Coverings | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L10-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L17-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L11-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |

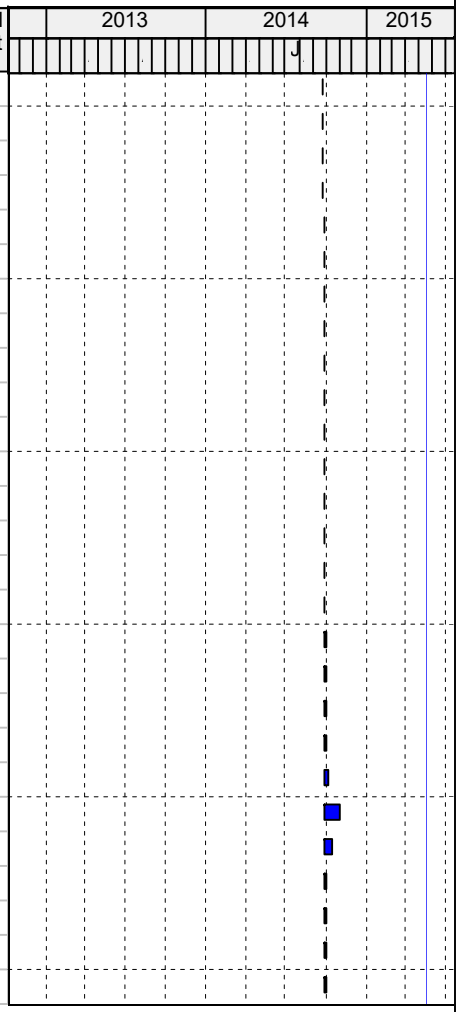



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L07-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 30-Sep-14 A | 08-Oct-14 A | |
| L11-8201 | Install ACT Grid @ Corridors | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L09-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L09-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L11-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L12-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L14-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L15-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| LL2-2072 | Generator - Complete generator and annunciator cor | 5 | 0 | 30-Sep-14 A | 21-Oct-14 A | |
| L17-6040 | Test Heat Pumps - L16 and L17 | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L17-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L14-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L03-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |

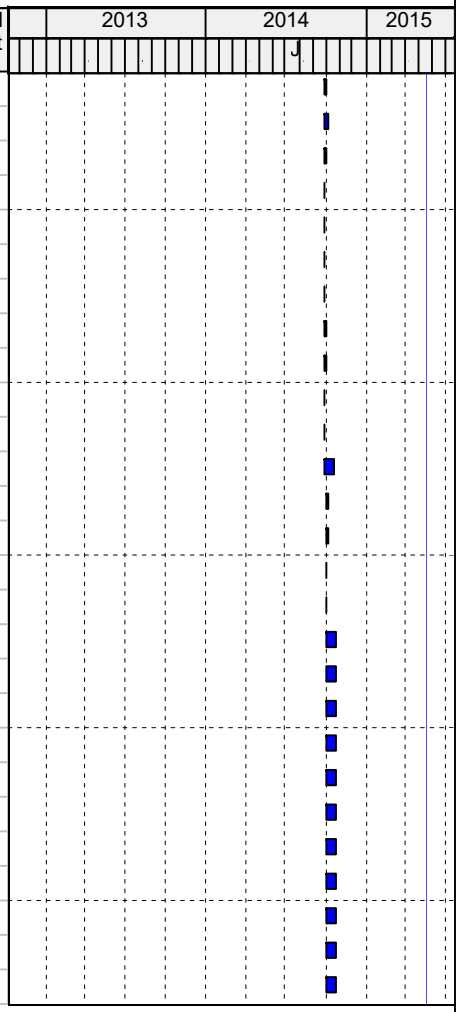



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L11-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |

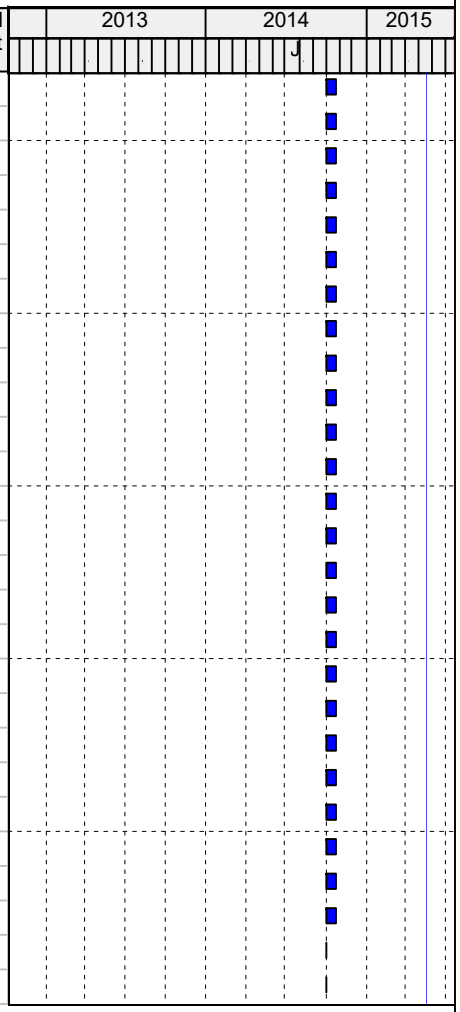



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L12-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L14-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L16-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L17-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L09-8136 | Install Counter Subtops | 3 | 0 | 01-Oct-14 A | 03-Oct-14 A | |
| L02-6032 | L2 - Electrical RI at Elevator Lobby & North Half | 5 | 0 | 01-Oct-14 A | 08-Oct-14 A | |
| SW-2306 | Prep, grind and overlay at 11th Ave, 3rd Place & 2nd | 5 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 01-Oct-14 A | 16-Dec-14 A | |
| L16-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L14-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L15-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1BOH2-8130 | Inspections For Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L02-6024a | L2 - Inspections - South Half | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L06-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| L17-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| LL2-2074 | Generator - Install fuel fill | 2 | 0 | 03-Oct-14 A | 06-Oct-14 A | |
| L07-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| MPT-1020 | Tower - Install E/W Wing, East End (Elev 41,44) | 5 | 0 | 06-Oct-14 A | 18-Oct-14 A | |
| LL1-8102a | GWB Hang/Tape (Ceilings) | 10 | 0 | 06-Oct-14 A | 18-Nov-14 A | |
| L1BOH2C-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |

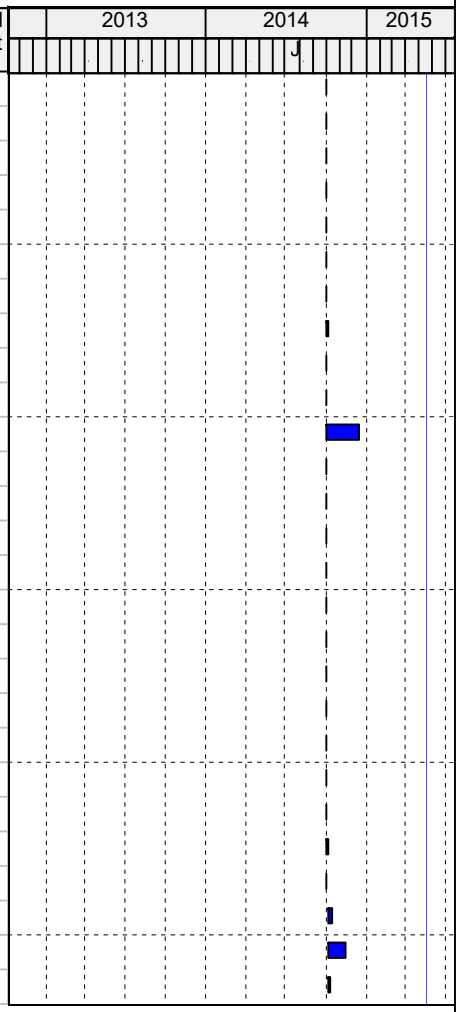



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1BOH2C-6014 | Complete Plumbing RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6016 | Complete Electrical RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6018 | Complete HVAC RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L03-8200a | New murals on site (date estimated) | 0 | 0 | 06-Oct-14 A | | |
| SW-2100 | Zone 1 - Survey curb & site lighting | 2 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 06-Oct-14 A | 06-Oct-14 A | |
| L1BOH2-8100 | Insulation | 4 | 0 | 07-Oct-14 A | 13-Oct-14 A | |
| L17-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L12-8201 | Install ACT Grid @ Corridors | 2 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| L10-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 07-Oct-14 A | 20-Oct-14 A | |
| L03-8216x | Vinyl Wall Coverings - Install Murals | 2 | 0 | 07-Oct-14 A | 29-Dec-14 A | |
| L1B-8102b | GWB Hang (Walls) & Inspection - Exterior Wall at Cor | 3 | 0 | 07-Oct-14 A | 09-Oct-14 A | |
| RF-4048 | Tower Roof - Install davit arms | 3 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| LL2-2076 | Generator - Install fuel fill mechanical piping | 4 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L12-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L09-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L03-8633 | Pool - Install waterproofing & test | 3 | 0 | 08-Oct-14 A | 17-Oct-14 A | |
| L03-8130 | Install Door Hardware | 3 | 0 | 08-Oct-14 A | 28-Oct-14 A | |
| L10-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L02-8102a | L2 - GWB Hang / Tape / Finish - South Half | 7 | 0 | 09-Oct-14 A | 27-Oct-14 A | |
| SW-2102 | Zone 1 - Vacate SE corner | 2 | 0 | 09-Oct-14 A | 11-Oct-14 A | |
| SW-2106 | Zone 1 - Sawcut and remove asphalt | 4 | 0 | 09-Oct-14 A | 14-Oct-14 A | |
| L11-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 09-Oct-14 A | |
| SW-2200 | Zone 2 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |
| SW-2300 | Zone 3 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |
| SW-2108 | Zone 1 - Install east footing drain | 4 | 0 | 10-Oct-14 A | 20-Oct-14 A | |

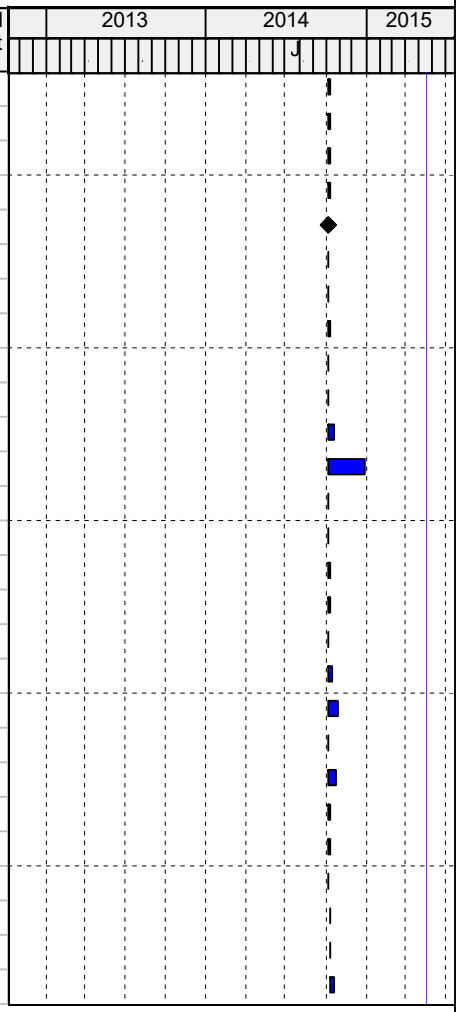



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8130 | Install Door Hardware | 3 | 0 | 10-Oct-14 A | 29-Oct-14 A | |
| ML-5962 | Man/Material Lifts - Remove Roof Lift Stop | 0 | 0 | | 11-Oct-14 A | |
| I-1102 | Additional work at new L17 guest rooms | 5 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| LL2-2046 | LL2 - Generator Room - Misc. Finishes | 3 | 0 | 13-Oct-14 A | 21-Nov-14 A | |
| RF-4008 | Tower Roof - Install corrugated metal panels | 5 | 0 | 13-Oct-14 A | 03-Nov-14 A | |
| MPT-1018b | Tower - Roof cornice frame & sheath | 6 | 0 | 13-Oct-14 A | 24-Oct-14 A | |
| L02-8100a | L2 - Insulation - South Half | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| SW-2112 | Zone 1 - Grade for curb and gutter | 3 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| SW-2202 | Zone 2 - Install site lighting | 5 | 0 | 13-Oct-14 A | 24-Nov-14 A | |
| SW-2204 | Zone 2 - Repave utility trenches | 4 | 0 | 13-Oct-14 A | 22-Oct-14 A | |
| L12-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 13-Oct-14 A | |
| I-5038 | RFI 735 - Landscape Irrigation Conflict | 1 | 0 | 13-Oct-14 A | 03-Nov-14 A | |
| SW-2302 | Zone 3 - Grade for curb and gutter | 2 | 0 | 14-Oct-14 A | 01-Dec-14 A | |
| L14-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 14-Oct-14 A | 16-Oct-14 A | |
| L05-8130 | Install Door Hardware | 3 | 0 | 14-Oct-14 A | 03-Nov-14 A | |
| L14-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 14-Oct-14 A | |
| I-5032 | RFI 715.1 - Additional Site Paving Per City | 1 | 0 | 14-Oct-14 A | 29-Oct-14 A | |
| L16-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L15-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 15-Oct-14 A | 17-Oct-14 A | |
| L15-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 15-Oct-14 A | |
| SW-2206 | Zone 2 - Grade for curb and gutter | 2 | 0 | 16-Oct-14 A | 20-Oct-14 A | |
| I-5598 | Resolve FCC hard lid ceiling issue (RFI 734) | 1 | 0 | 16-Oct-14 A | 16-Nov-14 A | |

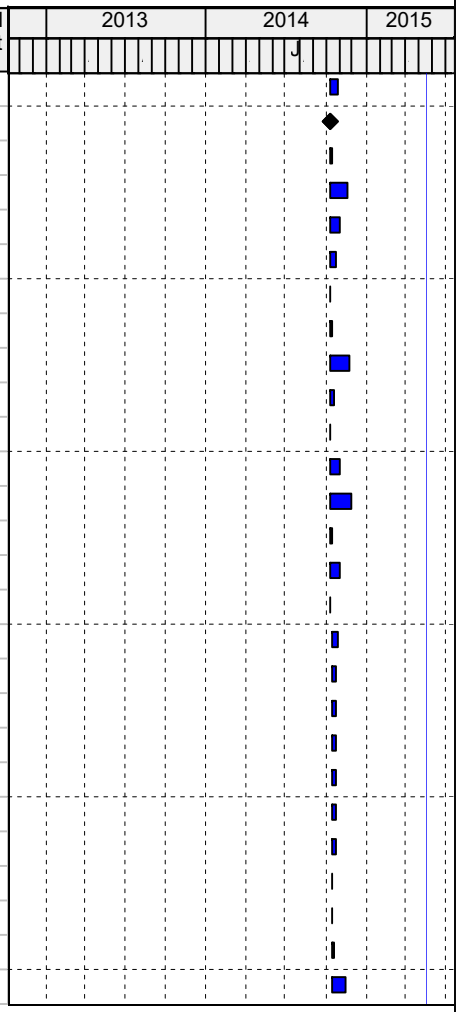



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ASI57 | ASI No. 57 - MDP Electrical Revisions Rev. 22 | 0 | 0 | 17-Oct-14 A | | |
| MPP-1000 | Podium - Install W/S/N Elevations (Elev 1-5, 6,9-19,2 | 10 | 0 | 20-Oct-14 A | 10-Dec-14 A | |
| L06-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 20-Oct-14 A | 23-Oct-14 A | |
| LL2-8106a | LL2, Garage - Pinned Insulation (except at ramp) | 4 | 0 | 20-Oct-14 A | 04-Dec-14 A | |
| L1B-8102d | GWB Hang (Walls) & Inspection - Main Ballroom East | 1 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| SW-2114 | Zone 1 - FRP curb and gutter | 2 | 0 | 20-Oct-14 A | 14-Nov-14 A | |
| RF-4044 | Ballroom Roof - Install metal coping | 3 | 0 | 20-Oct-14 A | 13-Nov-14 A | |
| L08-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 21-Oct-14 A | 23-Oct-14 A | |
| MPT-1018 | Tower - Install Roof Penthouse (Elev 36b,37,38.39) | 5 | 0 | 21-Oct-14 A | 05-Dec-14 A | |
| L11-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2208 | Zone 2 - FRP curb and gutter | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2304 | Zone 3 - FRP curb and gutter | 3 | 0 | 21-Oct-14 A | 02-Dec-14 A | |
| L15-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L06-8130 | Install Door Hardware | 3 | 0 | 21-Oct-14 A | 03-Nov-14 A | |
| I-5100 | Resolve changes (ASI's and RFI's) | 1 | 0 | 21-Oct-14 A | 07-Jan-15 A | |
| L03-8634 | Pool - Install reinforcing steel & inspect | 5 | 0 | 22-Oct-14 A | 30-Oct-14 A | |
| MPT-1016 | Tower - Install N/S Wing, S. End W. of Manlift (Elev 2 | 5 | 0 | 22-Oct-14 A | 05-Dec-14 A | |
| SW-2116 | Zone 1 - Fine grade for sidewalk | 3 | 0 | 22-Oct-14 A | 09-Mar-15 A | |
| LL4-8106 | LL4 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| LL3-8106 | LL3 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L14-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L08-8130 | Install Door Hardware | 3 | 0 | 22-Oct-14 A | 04-Nov-14 A | |
| L07-8130 | Install Door Hardware | 3 | 0 | 22-Oct-14 A | 03-Nov-14 A | |
| ASI54 | ASI No. 54 - Architectural Revisions for Lobby and Cl | 0 | 0 | 22-Oct-14 A | | |
| ASI55 | ASI No. 55 - Kay Lang Interior Concierge and Lobby | 0 | 0 | 22-Oct-14 A | | |
| L03-8606 | L3 Pool - HVAC R/I | 3 | 0 | 23-Oct-14 A | 27-Oct-14 A | |
| L09-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 23-Oct-14 A | 03-Nov-14 A | |

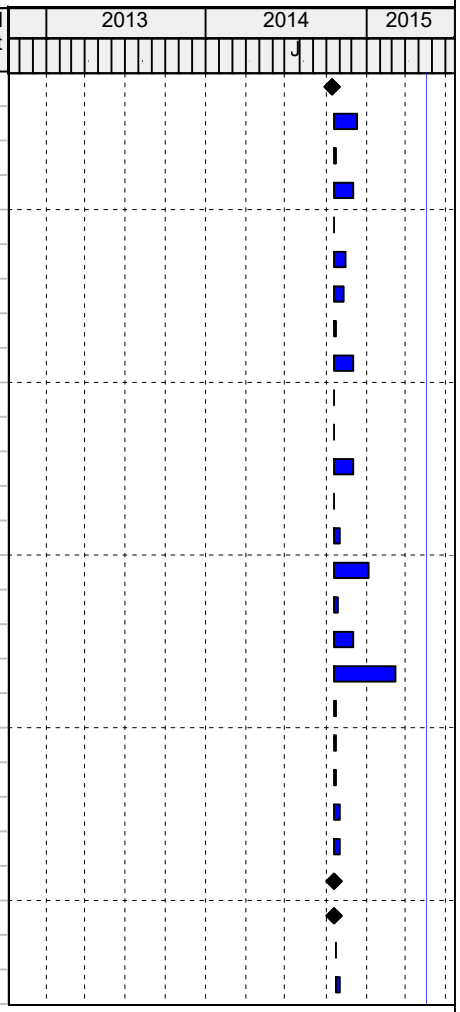



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| LL2-2078 | Generator - Install fuel fill control wiring | 2 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| I-2950 | Kitchen Hood Type 1 impact (COB correction notice, I | 1 | 0 | 23-Oct-14 A | 21-Dec-14 A | |
| RF-4050 | Roof at Manlift - Erect steel | 1 | 0 | 24-Oct-14 A | 24-Oct-14 A | |
| CO-7204 | Cx - Gas Service established | 0 | 0 | | 24-Oct-14 A | |
| I-5900 | Owner select color for Porte Cochere drive concrete | 20 | 0 | 24-Oct-14 A | 11-Mar-15 A | |
| L1BOH2-8102 | GWB Hang (Walls) | 4 | 0 | 27-Oct-14 A | 07-Nov-14 A | |
| L04-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 27-Oct-14 A | 12-Nov-14 A | |
| RF-4052 | Roof at Manlift - Framing/sheathing/air barrier (inspec | 4 | 0 | 27-Oct-14 A | 30-Oct-14 A | |
| LL2-2080 | Generator - Complete generator accessories (battery) | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| LL2-2082 | Generator - Cx fuel fill | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| L09-8130 | Install Door Hardware | 3 | 0 | 28-Oct-14 A | 04-Nov-14 A | |
| CO-7158 | Generator - Interim electrical inspection | 1 | 0 | 29-Oct-14 A | 29-Oct-14 A | |
| LL2-2070 | LL2 - Generator Room - Generator Ready for Startup | 0 | 0 | | 30-Oct-14 A | |
| LL2-2084 | Generator - Initial fuel fill | 1 | 0 | 30-Oct-14 A | 30-Oct-14 A | |
| CO-7200 | Cx - Penthouse Mechanical Installation Complete | 0 | 0 | | 30-Oct-14 A | |
| EL-6028 | Elev 6 - RFI-761: Response, pricing, complete work (r | 20 | 0 | 30-Oct-14 A | 27-Jan-15 A | |
| L03-8636 | Pool - Shotcrete | 1 | 0 | 31-Oct-14 A | 31-Oct-14 A | |
| RF-4054 | Roof at Manlift - Final mechanical installations | 4 | 0 | 31-Oct-14 A | 05-Nov-14 A | |
| RF-4056 | Roof at Manlift - Final electrical connections | 2 | 0 | 31-Oct-14 A | 05-Nov-14 A | |
| CO-7130 | Fire Alarm - Point-To-Point Wiring | 18 | 0 | 01-Nov-14 A | 06-Feb-15 A | |
| L03-8404 | GWB Hang/Tape Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 14-Nov-14 A | |
| L04-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 14-Nov-14 A | |
| L05-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 17-Nov-14 A | |
| L06-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 17-Nov-14 A | |
| L03-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L04-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |

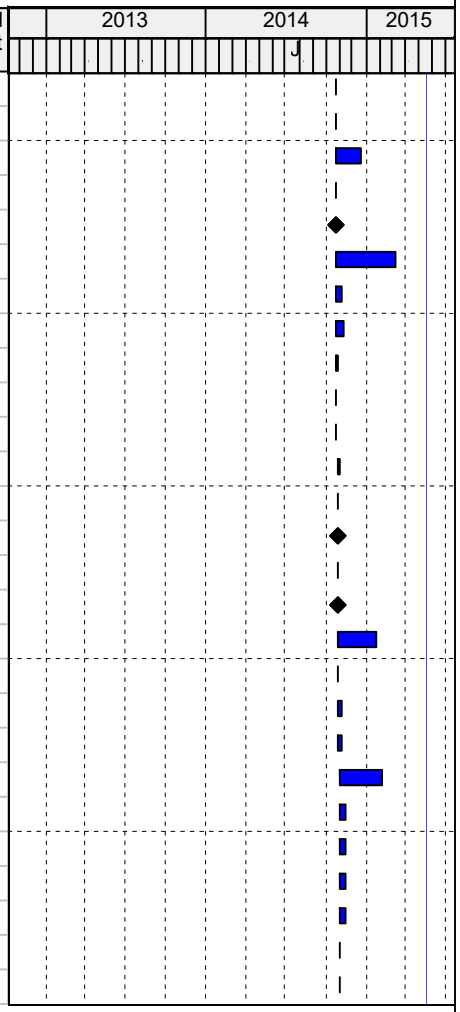


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L06-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L07-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L08-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L09-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L10-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L11-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L12-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L14-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L15-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L16-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L17-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L14-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 03-Nov-14 A | 06-Nov-14 A | |
| MPT-1024 | (A) Caulking - Elevation 41 (east elevation above poo | 7 | 0 | 03-Nov-14 A | 16-Dec-14 A | |
| CO-7206 | Cx - Purge/Prove Gas-Fed Equipment and Feeder Li | 7 | 0 | 03-Nov-14 A | 09-Nov-14 A | |
| I-5200 | Resolve MEP conflicts with ceiling grid (RFIs 783 & 8 | 8 | 0 | 03-Nov-14 A | 18-Mar-15 A | |
| I-5040 | RFI 776 - North Sidewalk-Entrance Conflicts | 1 | 0 | 03-Nov-14 A | 18-Dec-14 A | |
| L07-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 17-Nov-14 A | |
| L08-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L09-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L10-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L12-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L11-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 04-Nov-14 A | 15-Dec-14 A | |
| L11-8130 | Install Door Hardware | 3 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L10-8130 | Install Door Hardware | 3 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L11-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 18-Nov-14 A | |
| L12-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 19-Nov-14 A | |

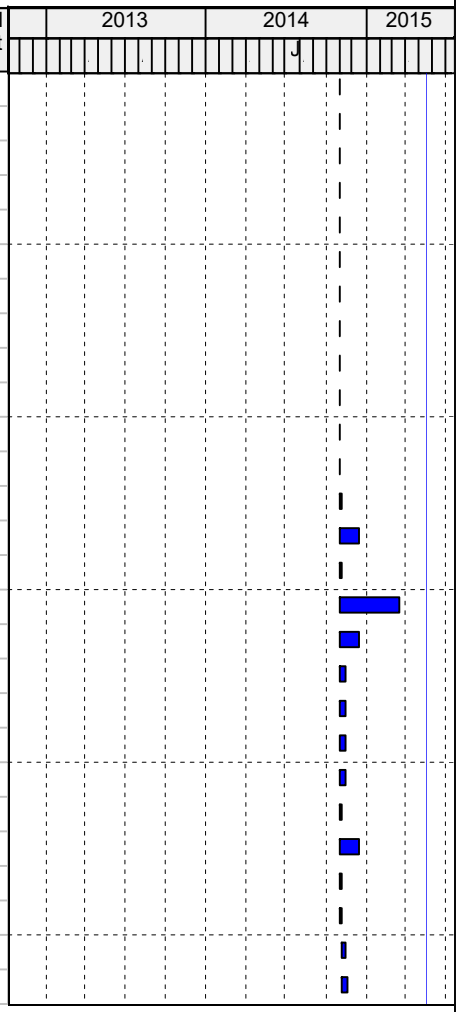



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 19-Nov-14 A | |
| MPP-1010 | Podium - Install East Elevation (Elev 5 & 7) | 7 | 0 | 05-Nov-14 A | 10-Dec-14 A | |
| CO-7162 | Generator - Load bank testing | 1 | 0 | 05-Nov-14 A | 05-Nov-14 A | |
| CO-7202 | Cx - Electrical Internal Bus & LL2-L17 Bus Duct Energ | 0 | 0 | | 05-Nov-14 A | |
| CO-7202a | Cx - Energize normal power distribution | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| I-5036 | RFI 717.1 - Porte Cochere Paving Details | 1 | 0 | 05-Nov-14 A | 26-Nov-14 A | |
| L15-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 19-Nov-14 A | |
| L16-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 20-Nov-14 A | |
| L17-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 20-Nov-14 A | |
| RF-4058 | Roof at Manlift - Install roofing | 2 | 0 | 06-Nov-14 A | 07-Nov-14 A | |
| CO-7164 | Generator - Final electrical inspection | 1 | 0 | 06-Nov-14 A | 06-Nov-14 A | |
| ASI59 | ASI No. 59 - Electrical One-Line Revisions | 0 | 0 | 06-Nov-14 A | | |
| I-5042 | RFI 796 - City Requested Added Scope | 1 | 0 | 06-Nov-14 A | 22-Dec-14 A | |
| I-5046 | RFI 803 - Site Light Bases Layout with Existing Sidew | 1 | 0 | 06-Nov-14 A | 14-Jan-15 A | |
| L15-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 07-Nov-14 A | 12-Nov-14 A | |
| L03-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L03-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L04-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L04-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L05-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L05-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L06-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L06-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L07-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L07-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L08-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L08-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |

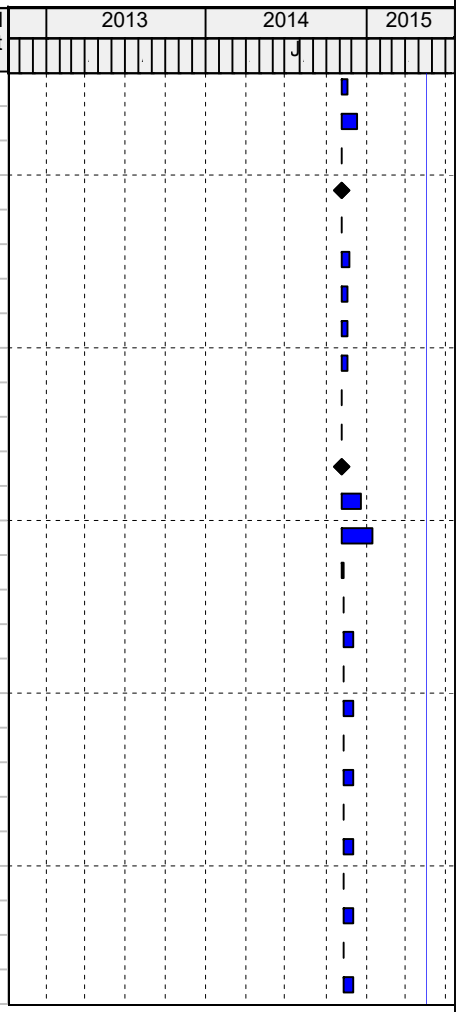



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L09-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L10-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L10-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L11-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L11-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L12-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L12-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L14-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L14-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L15-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L15-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L16-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L16-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L17-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L17-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L05-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| L06-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 10-Nov-14 A | 11-Nov-14 A | |
| MPT-1032 | Tower - Install sign backing NW (Elev 51,52) | 4 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L12-8130 | Install Door Hardware | 3 | 0 | 10-Nov-14 A | 12-Nov-14 A | |
| EL-1230 | Elev 1&2 - Complete hoistway ventilation | 13 | 0 | 10-Nov-14 A | 15-Dec-14 A | |
| EL-1232 | Elev 1&2 - Wire & startup AC split units | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-1234 | Elev 1&2 - Install EMR doors, hardware & labeling | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-3428 | Elev 3&4 - Complete hoistway ventilation | 13 | 0 | 10-Nov-14 A | 15-Dec-14 A | |
| EL-3430 | Elev 3&4 - Wire & startup AC split units | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-3432 | Elev 3&4 - Install EMR doors, hardware & labeling | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-6030 | Elev 6 - Complete fire-rated assemblies at hoistway, l | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |

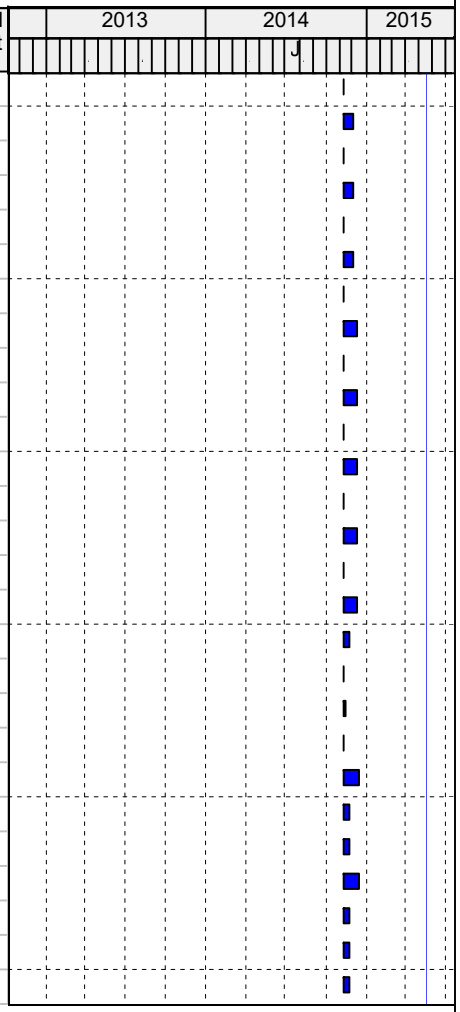



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 11-Nov-14 A | 12-Nov-14 A | |
| L16-8106 | Paint - Accent Walls | 2 | 0 | 11-Nov-14 A | 12-Nov-14 A | |
| L14-8130 | Install Door Hardware | 3 | 0 | 11-Nov-14 A | 13-Nov-14 A | |
| I-5044 | RFI 802 - Landscape Planter & Arch Detail Coordinati | 1 | 0 | 11-Nov-14 A | 18-Nov-14 A | |
| L03-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 12-Nov-14 A | 18-Nov-14 A | |
| SW-2104 | Zone 1 - Install lighting conduit at SE corner | 2 | 0 | 12-Nov-14 A | 14-Nov-14 A | |
| L16-8111 | Paint - Door Jambs | 2 | 0 | 12-Nov-14 A | 13-Nov-14 A | |
| EL-6010i | Elev 6 - Pit Slab Correction (form/pour/strip/clean) | 10 | 0 | 12-Nov-14 A | 26-Nov-14 A | |
| SW-2024 | Zone 4 - FRP Porte Cochere planter & bench | 6 | 0 | 12-Nov-14 A | 04-Dec-14 A | |
| L08-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| SW-2109 | Zone 1 - Install irrigation sleeves | 2 | 0 | 13-Nov-14 A | 14-Nov-14 A | |
| MPT-1026 | (C) Caulking - Elevation 47 (north elevation, east half | 10 | 0 | 13-Nov-14 A | 19-Dec-14 A | |
| L16-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| L15-8130 | Install Door Hardware | 3 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| ASI56 | ASI No. 56 - Interior Design Millwork and Finish Chan | 0 | 0 | 13-Nov-14 A | | |
| L04-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 14-Nov-14 A | 19-Nov-14 A | |
| SW-2203 | Zone 2 - Install irrigation sleeves | 2 | 0 | 14-Nov-14 A | 08-Jan-15 A | |
| L1B-8120 | Install operable partitions | 3 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| LL1-Z3-8340 | Install walk-in cooler/freezer (BY OTHERS) | 5 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| SW-2316 | Zone 3 - Demolish manlift shack and base | 5 | 0 | 17-Nov-14 A | 20-Nov-14 A | |
| I-1610 | Enclosure at manlift - Install exterior wall panels & ins | 5 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| L04-8140 | Install window sills | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| L03-8140x | Install window sills | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| L16-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| SW-2014 | Porte Cochere - Electrical rough-in | 5 | 0 | 17-Nov-14 A | 08-Dec-14 A | |
| I-5600 | Lower heat pump and install access panels (RFI 734) | 13 | 0 | 17-Nov-14 A | 09-Jan-15 A | |
| LL1-Z3-FCC26 | Program FACP & Stand-Up System | 20 | 0 | 17-Nov-14 A | 22-Jan-15 A | |

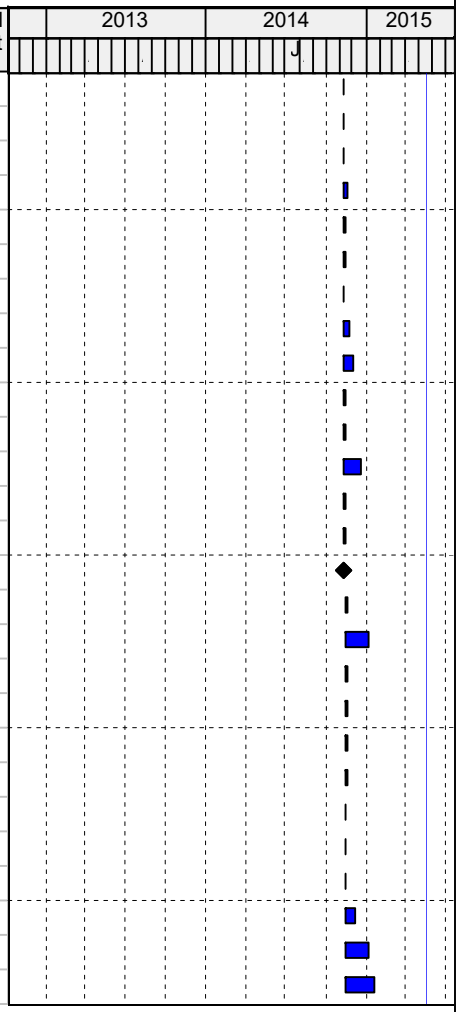



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8140 | Install window sills | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L05-8140 | Install window sills | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| I-5048 | RFI 805 - City Approved Public ROW Irrigation Lines M | 1 | 0 | 18-Nov-14 A | 05-Dec-14 A | |
| L05-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 19-Nov-14 A | 22-Dec-14 A | |
| L16-8130 | Install Door Hardware | 3 | 0 | 19-Nov-14 A | 02-Dec-14 A | |
| L08-8140 | Install window sills | 2 | 0 | 19-Nov-14 A | 19-Nov-14 A | |
| L07-8140 | Install window sills | 2 | 0 | 19-Nov-14 A | 19-Nov-14 A | |
| I-1616 | Enclosure at manlift - Patch/repair concrete shear wal | 3 | 0 | 19-Nov-14 A | 21-Nov-14 A | |
| ASI58 | ASI No. 58 - Level 1 Valet Phone and POS Locations | 0 | 0 | 19-Nov-14 A | | |
| ASI59ca | ASI No. 59 - Electrical One-Line Revisions (City Appro | 0 | 0 | 19-Nov-14 A | | |
| L10-8140 | Install window sills | 2 | 0 | 20-Nov-14 A | 20-Nov-14 A | |
| L09-8140 | Install window sills | 2 | 0 | 20-Nov-14 A | 20-Nov-14 A | |
| I-1622 | Manlift finishes - Install windows & caulk | 4 | 0 | 20-Nov-14 A | 03-Dec-14 A | |
| LL2-2060 | LL2 - Paint Laundry Room | 3 | 0 | 21-Nov-14 A | 24-Nov-14 A | |
| L03-8616 | L3 Pool - GWB above ceiling | 2 | 0 | 21-Nov-14 A | 22-Nov-14 A | |
| LL1-Z3-8342 | Final connections at walk-in cooler/freezer | 2 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L1K-8340 | Install walk-in cooler/freezer (BY OTHERS) | 2 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L10-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| L16-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| SW-2110 | Zone 1 - Adjust utilities structures | 5 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| SW-2214 | Zone 2 - Adjust utilities structures | 2 | 0 | 24-Nov-14 A | 25-Nov-14 A | |
| MPT-1030 | Tower - Install sign backing NE (Elev 44) | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| SW-2012 | Porte Cochere - Install cornice[DELETED SEE REV M | 8 | 0 | 24-Nov-14 A | 05-Dec-14 A | |
| L03-8650 | L3 Pool - Build scaffold at pool pit | 2 | 0 | 24-Nov-14 A | 25-Nov-14 A | |
| EL-6032 | Elev 6 - Install pit ladder | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| EL-6034 | Elev 6 - Install pit jack & hoistway pistons; connect hy | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| L06-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 25-Nov-14 A | 22-Dec-14 A | |

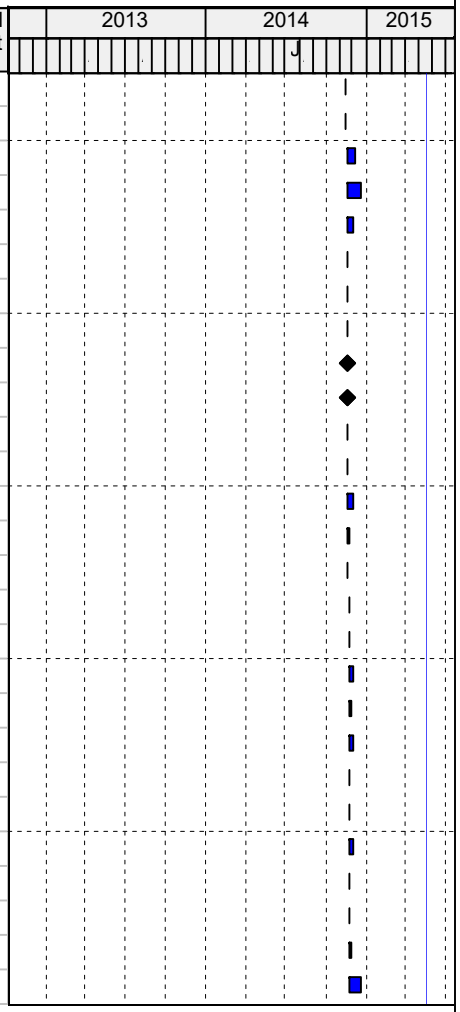



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8104a | L2 - Int Painting - South Half | 2 | 0 | 25-Nov-14 A | 26-Nov-14 A | |
| SW-2016 | Porte Cochere - Complete framing | 3 | 0 | 25-Nov-14 A | 01-Dec-14 A | |
| LL2-2096 | LL2 - Install FRP at Laundry Room | 8 | 0 | 25-Nov-14 A | 05-Dec-14 A | |
| I-1602 | Enclosure at manlift - Install shear wall clips and inspe | 4 | 0 | 26-Nov-14 A | 05-Dec-14 A | |
| L07-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| SW-2318 | Zone 3 - Install catch basin | 1 | 0 | 26-Nov-14 A | 26-Nov-14 A | |
| L03-8652 | L3 Pool - Frame ceiling | 4 | 0 | 26-Nov-14 A | 04-Dec-14 A | |
| I-5052 | RFI 819 - Flagpole Locations | 1 | 0 | 26-Nov-14 A | 30-Dec-14 A | |
| I-5050 | RFI 818 - 111th East Elevation Hardscape Vertical Dif | 1 | 0 | 26-Nov-14 A | 29-Dec-14 A | |
| L03-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L04-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L05-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L06-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L07-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L09-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L10-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L11-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L12-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L14-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L15-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L16-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L17-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 01-Dec-14 A | 04-Dec-14 A | |
| L02-6016a | L2 - Electrical Room Buildout | 5 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| L03-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L04-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |

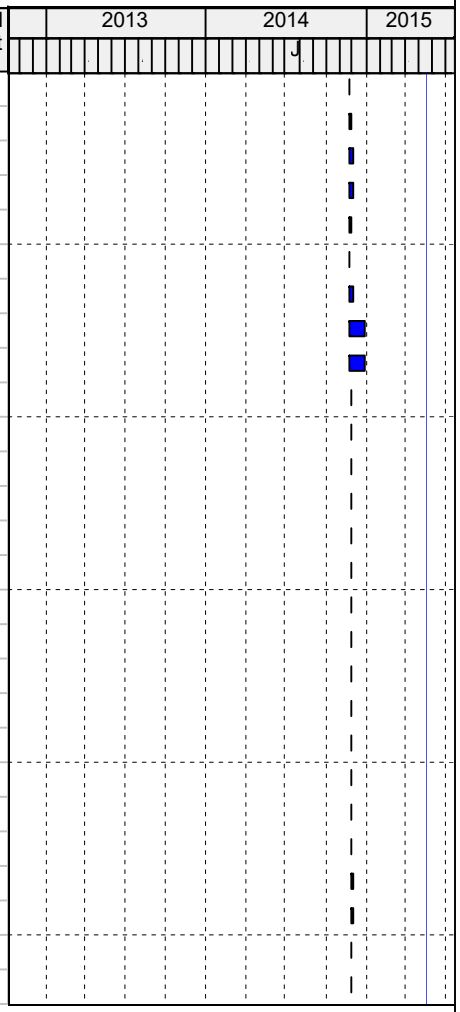



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L06-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L07-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L09-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L10-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L11-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L12-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L14-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L15-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L16-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L17-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| SW-2210 | Zone 2 - Fine grade for sidewalk | 5 | 0 | 01-Dec-14 A | 08-Jan-15 A | |
| RF-4040 | L2.5 Horseshoe - Install sheet metal capping[DELETI | 3 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| MPT-1042 | Enclosure at manlift - air barrier & inspect | 5 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| CO-7208 | Cx - Start-Up Pumps | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| CO-7210 | Cx - Start-Up VFD's | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| L17-8106 | Paint - Accent Walls | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| LL4-8116 | LL4 - Install ACT grid [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL3-8116 | LL3 - Install ACT grid [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| I-1630 | Manlift finishes - Framing, corridor ceilings & inspect | 4 | 0 | 01-Dec-14 A | 09-Dec-14 A | |
| EL-6036 | Elev 6 - Install shunt trip breaker | 5 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| L17-8111 | Paint - Door Jambs | 2 | 0 | 02-Dec-14 A | 03-Dec-14 A | |
| SW-2018 | Porte Cochere - GWB hang/tape | 3 | 0 | 02-Dec-14 A | 09-Dec-14 A | |
| L03-8654 | L3 Pool - HVAC drops at ceiling & inspect | 3 | 0 | 02-Dec-14 A | 05-Dec-14 A | |
| L11-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 03-Dec-14 A | 08-Dec-14 A | |
| SW-2308 | Zone 3 - Install site lighting | 5 | 0 | 03-Dec-14 A | 04-Dec-14 A | |

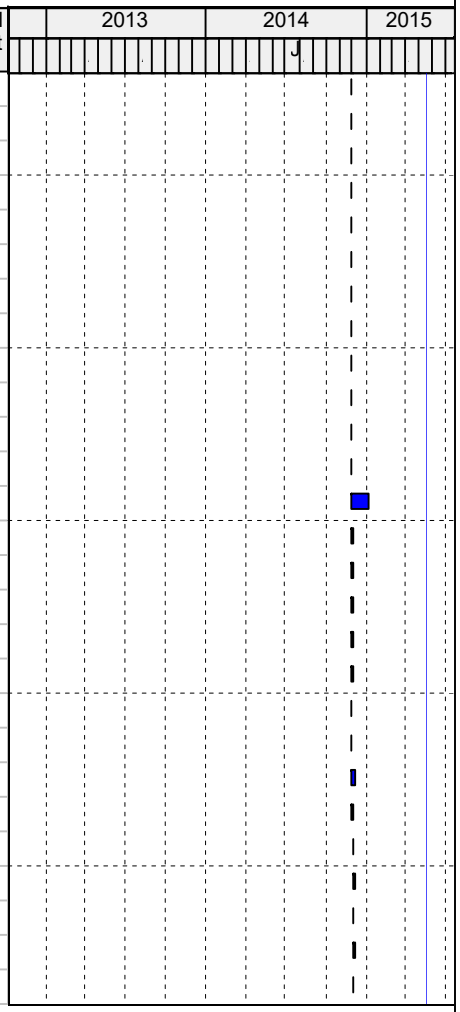



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 03-Dec-14 A | 15-Dec-14 A | |
| I-1632 | Manlift finishes - Electrical rough-in & inspect | 2 | 0 | 03-Dec-14 A | 10-Dec-14 A | |
| SW-2028 | Zone 4 - Scan Porte Cochere deck | 2 | 0 | 04-Dec-14 A | 05-Dec-14 A | |
| I-1624 | Manlift finishes - Install batt insulation & inspect | 2 | 0 | 04-Dec-14 A | 04-Dec-14 A | |
| I-1626 | Manlift finishes - Shim window openings | 2 | 0 | 04-Dec-14 A | 05-Dec-14 A | |
| I-1628 | Manlift finishes - Install vapor barrier & inspect | 2 | 0 | 04-Dec-14 A | 08-Dec-14 A | |
| I-5054 | RFI 832.1 - South Elevation Emergency Exit with Side | 1 | 0 | 04-Dec-14 A | 18-Dec-14 A | |
| I-1608 | Tower - Install N/S Wing, S. End at manlift (Elev 32) [I | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1012 | Tower - Install N/S Wing, S. End E. Side Concrete (El | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| PC-4012 | Porte Cochere - Install sheet metal capping[DELETEI | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4046 | Tower Roof - Install sheet metal capping[DELETED S | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4060 | Roof at Manlift - Install corrugated metal panels[DELE | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4062 | Roof at Manlift - Install sheet metal capping[DELETEI | 2 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4064 | Pool Green Roof - Install sheet metal capping[DELET | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1040 | Tower - Install N/S Wing, S, End (Elev 30)[DELETED | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1044 | Enclosure at manlift - Install sign backing south[DELE | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1612 | Enclosure at manlift - Caulking[DELETED SEE REV M | 8 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1614 | Enclosure at manlift - Install rigid insulation at shear w | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1618 | Enclosure at manlift - Install framing at shear wall[DEI | 5 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1620 | Enclosure at manlift - Install hat channel over framing | 5 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| L03-8656 | L3 Pool - Electrical rough-in at ceiling & inspect | 3 | 0 | 05-Dec-14 A | 19-Dec-14 A | |
| I-5058 | RFI 834 - NE Retaining Wall Design Clarifications | 1 | 0 | 05-Dec-14 A | 23-Dec-14 A | |
| I-5062 | RFI 835 - NW Planter Wall Drainage | 1 | 0 | 05-Dec-14 A | 10-Dec-14 A | |
| L1K-8344 | Set kitchen hoods | 8 | 0 | 06-Dec-14 A | 21-Dec-14 A | |
| L12-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L03-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |
| L04-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |

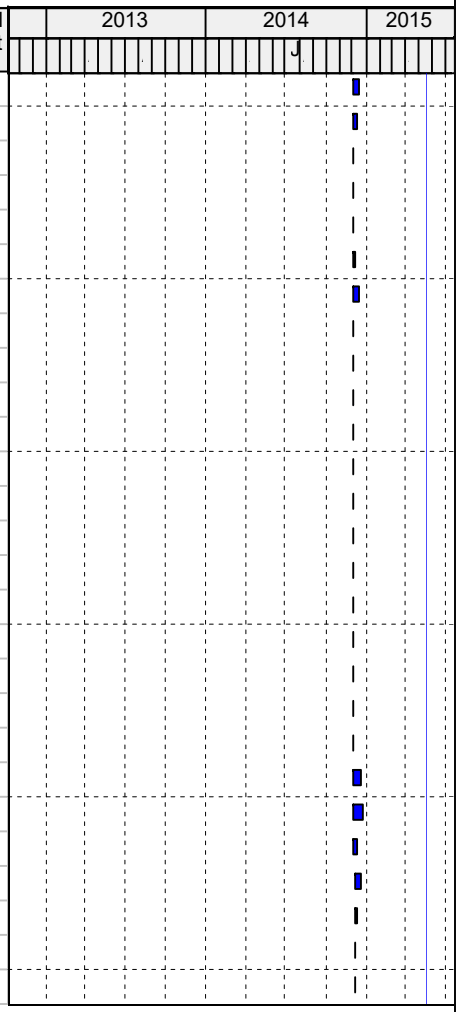



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |
| SW-2312 | Zone 3 - Fine grade for sidewalk | 3 | 0 | 08-Dec-14 A | 08-Jan-15 A | |
| RF-4042 | Pool Roof - Install metal coping at high roof | 2 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L17-8130 | Install Door Hardware | 3 | 0 | 08-Dec-14 A | 11-Dec-14 A | |
| L09-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L03-8658 | L3 Pool - Fire sprinkler drops at ceiling & inspect | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| LL2-8140 | LL2 - Install vinyl wall coverings | 2 | 0 | 08-Dec-14 A | 24-Dec-14 A | |
| L04-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L05-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L07-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L08-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L14-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L15-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 09-Dec-14 A | 12-Dec-14 A | |
| L03-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L07-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L08-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L04-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L05-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L07-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L08-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |

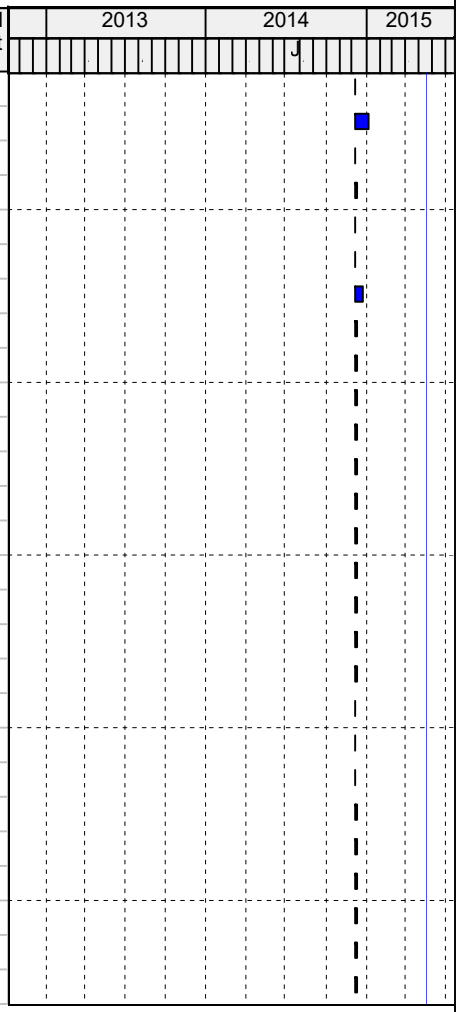



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| RF-4072 | Pool Roof - Install metal coping | 3 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L17-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 09-Dec-14 A | 12-Dec-14 A | |
| L07-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 09-Dec-14 A | 29-Dec-14 A | |
| L06-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 09-Dec-14 A | 24-Dec-14 A | |
| I-1604 | Manlift finishes - GWB, hang walls | 2 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L07-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L08-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 16-Dec-14 A | |
| L11-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L12-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L14-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L15-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L16-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L17-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| LL2E-8340 | LL2 - Install walk-in cooler/freezer (BY OTHERS) | 5 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L10-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 10-Dec-14 A | 17-Dec-14 A | |
| L09-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L10-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L11-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L11-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L12-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L14-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L15-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L16-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L17-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L08-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 10-Dec-14 A | 29-Dec-14 A | |
| I-1634 | Manlift finishes - GWB, hang ceilings | 2 | 0 | 10-Dec-14 A | 16-Dec-14 A | |

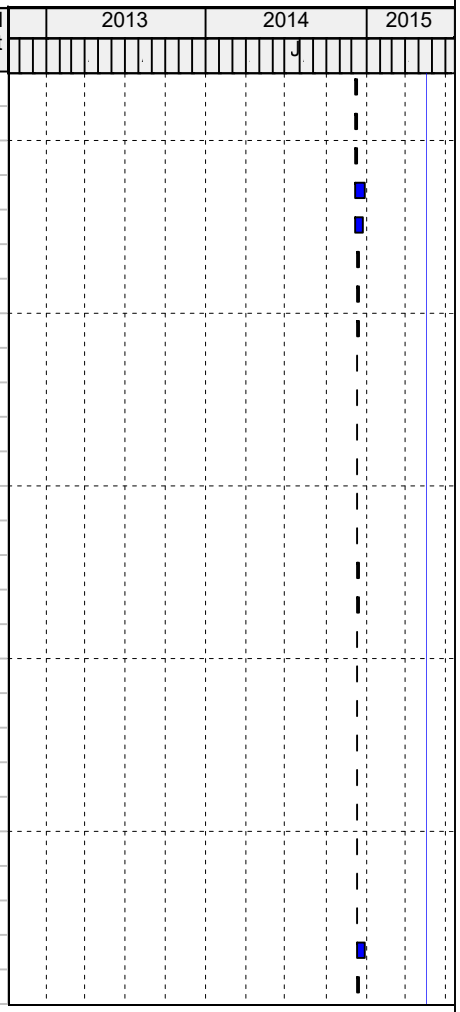



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L14-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L15-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L03-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L04-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| MPT-1034 | (A) Elevation 52 (west elevation, north end, L3-L18) | 4 | 0 | 11-Dec-14 A | 16-Dec-14 A | |
| MPT-1036 | (B) Elevation 45/46 (north elevation, east end, L3-L1 | 5 | 0 | 11-Dec-14 A | 19-Dec-14 A | |
| L16-7030 | Paint | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L17-7030 | Paint | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L05-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L06-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| MPT-1066 | Tower Sign, East (El. 32) - Install backing | 3 | 0 | 12-Dec-14 A | 22-Dec-14 A | |
| MPT-1076 | (B) Caulking - Elevation 51 (north elevation, west half | 10 | 0 | 12-Dec-14 A | 19-Dec-14 A | |
| L04-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L04-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L07-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L08-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L09-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L14-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L15-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L17-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 16-Dec-14 A | |
| L04-7042 | Install Tile Flooring (x41) | 2 | 0 | 15-Dec-14 A | 24-Dec-14 A | |
| L05-7042 | Install Tile Flooring (x41) | 2 | 0 | 15-Dec-14 A | 24-Dec-14 A | |

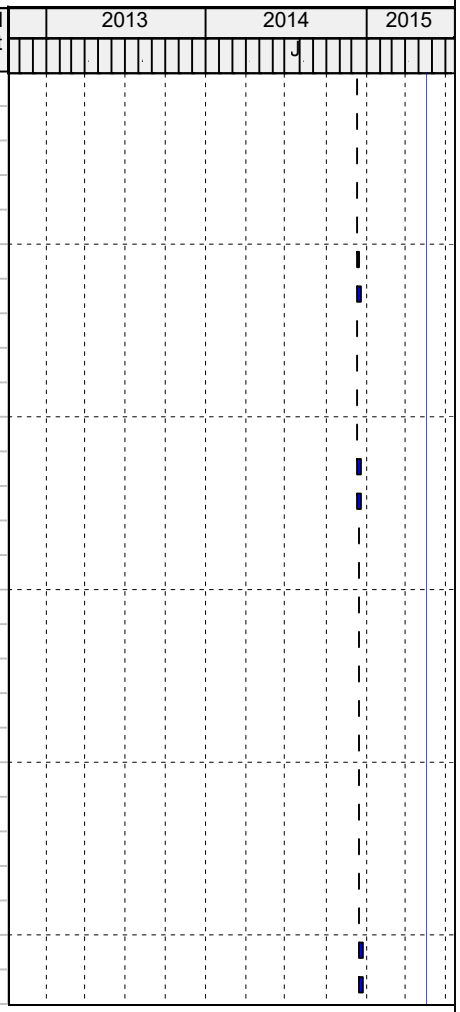



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8102a | LL4 - GWB Tape/Finish | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| LL3-8102a | LL3 - GWB Tape/Finish | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| L03-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L04-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L07-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L08-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L09-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L10-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| CO-7126 | Fire pump test pre-planning complete (see checklist) | 0 | 0 | | 15-Dec-14 A | |
| LL1-Z3-6034 | COB Correction - Add ceiling access panels in Food F | 10 | 0 | 15-Dec-14 A | 26-Jan-15 A | |
| L03-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| L05-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L09-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L10-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L10-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L11-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L11-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L14-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L15-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L16-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L17-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| LL2E-8342 | LL2 - Final connections at walk-in cooler/freezer | 5 | 0 | 16-Dec-14 A | 05-Jan-15 A | |
| L11-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 16-Dec-14 A | 18-Dec-14 A | |

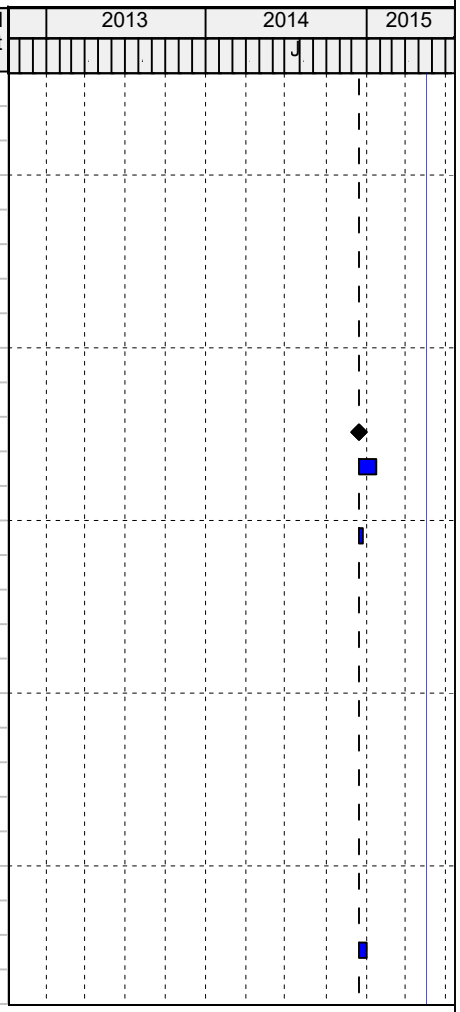



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8201 | Corridors - Install ACT Grid | 2 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L06-7042 | Install Tile Flooring (x41) | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L07-7042 | Install Tile Flooring (x41) | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| LL1-Z2-8102a | GWB Hang (Ceilings) & Inspection | 3 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L11-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L14-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L15-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L16-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L17-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| CO-7128 | Run fire pump test | 2 | 0 | 16-Dec-14 A | 17-Dec-14 A | |
| L09-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 16-Dec-14 A | 30-Dec-14 A | |
| SW-2026 | Zone 4 - FRP NW planter | 5 | 0 | 16-Dec-14 A | 05-Jan-15 A | |
| I-5370 | (S) Resolve south tower sign backing (RFI 844) | 5 | 0 | 16-Dec-14 A | 09-Jan-15 A | |
| L03-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 22-Dec-14 A | |
| L04-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 23-Dec-14 A | |
| L06-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 29-Dec-14 A | |
| L07-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 30-Dec-14 A | |
| L08-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 31-Dec-14 A | |
| L09-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 05-Jan-15 A | |
| L14-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L15-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L16-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L17-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L08-7042 | Install Tile Flooring (x41) | 2 | 0 | 17-Dec-14 A | 24-Dec-14 A | |
| L09-7042 | Install Tile Flooring (x41) | 2 | 0 | 17-Dec-14 A | 24-Dec-14 A | |
| L04-7136 | Install Door and Hardware | 1 | 0 | 17-Dec-14 A | 17-Dec-14 A | |

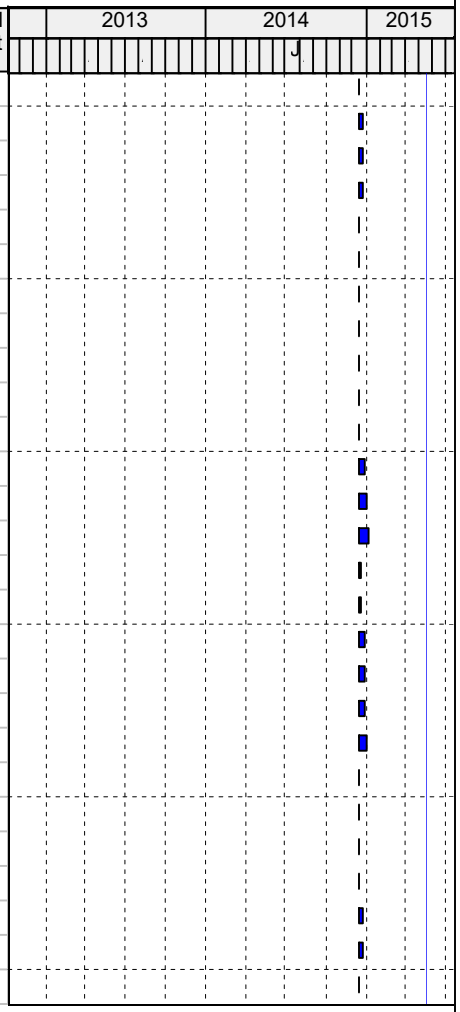



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 17-Dec-14 A | 29-Dec-14 A | |
| MPT-1046 | (A) Elevation 26/27/53 (west elevation, south of 52, L | 3 | 0 | 17-Dec-14 A | 18-Dec-14 A | |
| MPT-1057 | (S) Elevation 32 framing (south elevation, east of mai | 5 | 0 | 17-Dec-14 A | 19-Jan-15 A | |
| MPT-1080 | (A) Caulking - Elevation 44 (east elevation above poo | 8 | 0 | 17-Dec-14 A | 22-Dec-14 A | |
| LL1-Z2-8108 | Framing, ceiling clouds (incl. inspection) | 5 | 0 | 17-Dec-14 A | 22-Jan-15 A | |
| MPP-1006 | (C) Install Level 3 cornice metal (north, west & south) | 6 | 0 | 18-Dec-14 A | 30-Jan-15 A | |
| L10-7042 | Install Tile Flooring (x41) | 2 | 0 | 18-Dec-14 A | 24-Dec-14 A | |
| L11-7042 | Install Tile Flooring (x41) | 2 | 0 | 18-Dec-14 A | 24-Dec-14 A | |
| L12-7042 | Install Tile Flooring (x41) | 2 | 0 | 19-Dec-14 A | 24-Dec-14 A | |
| L14-7042 | Install Tile Flooring (x41) | 2 | 0 | 19-Dec-14 A | 24-Dec-14 A | |
| MPT-1048 | (B) Elevation 37 (penthouse east) | 3 | 0 | 19-Dec-14 A | 20-Dec-14 A | |
| I-5000 | Resolve RFI's and site work changes (new drawings) | 10 | 0 | 19-Dec-14 A | 02-Mar-15 A | |
| I-5002 | Resolve RFI's and site work changes (new drawings) | 20 | 0 | 19-Dec-14 A | 09-Feb-15 A | |
| I-5003 | Resolve RFI's and site work changes (new drawings) | 10 | 0 | 19-Dec-14 A | 02-Mar-15 A | |
| I-5004 | Resolve RFI's and site work changes (new drawings) | 1 | 0 | 19-Dec-14 A | 16-Jan-15 A | |
| I-5064 | RFI 848 - Lighting at Flagpole Locations | 1 | 0 | 19-Dec-14 A | 14-Jan-15 A | |
| L03-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 22-Dec-14 A | 22-Dec-14 A | |
| L07-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L17-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| CO-7212 | Cx - Start-Up Boilers | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L17-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L08-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L07-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L06-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L05-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L04-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 22-Dec-14 A | |
| I-1636 | Manlift finishes - GWB, tape & finish | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |

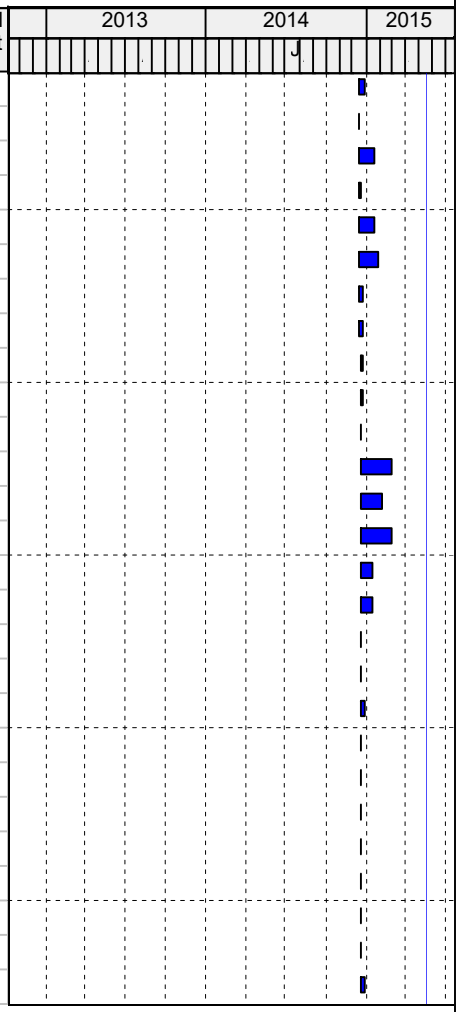



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6038 | Elev 6 - Rough-in call boxes & lanterns | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| EL-6052 | Elev 6 - Complete hoistway ventilation | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| MPT-1078 | (C) Caulking - Elevation 37/38/39 (penthouse) | 4 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| MPT-1086 | (A) Caulking - Elevation 45/46 (north elevation, east e | 7 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| MPT-1088 | (B) Caulking - Elevation 52/53/26/27 (west elevation, | 11 | 0 | 22-Dec-14 A | 02-Jan-15 A | |
| MPP-1044 | Caulking - Elevation 9/10/11/12/13 (upper ballroom) | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| MPP-1046 | Caulking - Elevation 5/6 (east elevation, south end) | 8 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| I-5068 | RFI 857 - South Elevation Landscape & Irrigation Re | 1 | 0 | 22-Dec-14 A | 07-Jan-15 A | |
| I-5070 | RFI 858 - North Elevation Landscape & Irrigation Req | 1 | 0 | 22-Dec-14 A | 07-Jan-15 A | |
| I-5072 | RFI 859 - Additional Curbs at Openings (see RFI 776) | 1 | 0 | 22-Dec-14 A | 07-Jan-15 A | |
| L03-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L03-7032 | Install VCT Flooring (x42) | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L08-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L10-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L09-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| ASI62 | ASI No. 62 - Civil Site Grading Revisions | 0 | 0 | 23-Dec-14 A | | |
| I-5074 | RFI 860 - SE Corner Hardscape Additional Clarificatio | 1 | 0 | 23-Dec-14 A | 07-Jan-15 A | |
| L09-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 24-Dec-14 A | 29-Dec-14 A | |
| L03-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 31-Dec-14 A | |
| L15-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L16-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L17-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L04-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L05-7136 | Install Door and Hardware | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L10-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L17-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| LL1-Z3-8202 | Install FRP wall coverings | 4 | 0 | 29-Dec-14 A | 06-Jan-15 A | |

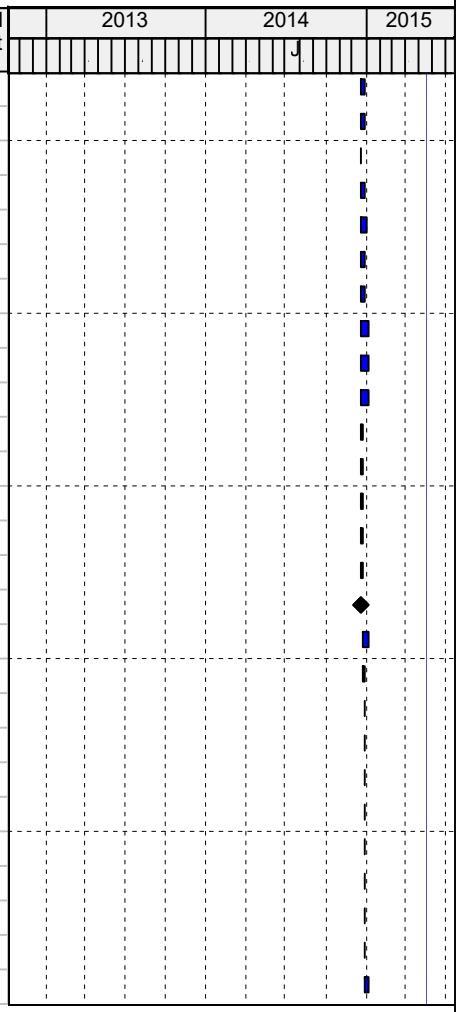



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L05-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L06-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L07-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L08-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L09-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L10-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL2-8130 | LL2 - Install ceiling grid | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| I-5300 | Heat Pump Revision - demo existing ceiling framing | 2 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L12-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 30-Dec-14 A | 05-Jan-15 A | |
| L06-7136 | Install Door and Hardware | 1 | 0 | 30-Dec-14 A | 30-Dec-14 A | |
| L11-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 30-Dec-14 A | 31-Dec-14 A | |
| I-5302 | Heat Pump Revision - rework MEP at celing | 5 | 0 | 30-Dec-14 A | 12-Jan-15 A | |
| I-1606 | Manlift finishes - Prime & paint | 4 | 0 | 31-Dec-14 A | 06-Jan-15 A | |
| L07-7136 | Install Door and Hardware | 1 | 0 | 31-Dec-14 A | 31-Dec-14 A | |
| L12-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 31-Dec-14 A | 05-Jan-15 A | |
| CO-7214 | Cx - Flush & Fill HVAC Hydronics Systems | 5 | 0 | 02-Jan-15 A | 05-Jan-15 A | |
| MPP-1032 | (C) Elevation 23/24/25 (Porte Cochere north, below c | 5 | 0 | 02-Jan-15 A | 19-Jan-15 A | |
| L1BOH2-8215 | GWB tape & finish walls & ceilings | 7 | 0 | 05-Jan-15 A | 02-Mar-15 A | |
| L10-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| L11-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 13-Jan-15 A | |
| L12-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 13-Jan-15 A | |
| L14-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| L16-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L04-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L05-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L06-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |

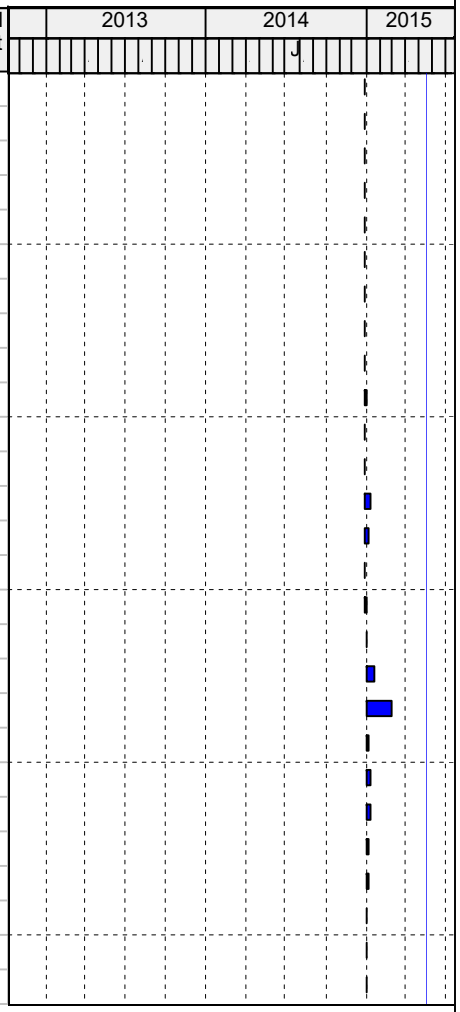



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| L06-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L07-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L08-7136 | Install Door and Hardware | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L08-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L09-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L10-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L14-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| SW-2314 | Zone 3 - FRP sidewalk | 5 | 0 | 05-Jan-15 A | 16-Feb-15 A | |
| L10-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 05-Jan-15 A | 27-Jan-15 A | |
| CO-7240 | Cx - Heat Pump Start-Up - Levels 3 & 4 | 5 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| SW-2220 | Zone 2 - FRP curb/gutter at NW corner | 4 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| MPT-1054 | Complete Elevation 30 (south elevation, west of man | 5 | 0 | 05-Jan-15 A | 18-Mar-15 A | |
| MPP-1028 | (C) Tapered pilasters, west | 3 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| MPP-1030 | (C) Tapered pilasters, east | 3 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| LL2-8142 | HVAC drops/trim to grid | 3 | 0 | 05-Jan-15 A | 19-Jan-15 A | |
| L1L-8216 | Complete electrical/fire alarm drops @ ceilings | 5 | 0 | 05-Jan-15 A | 08-Jan-15 A | |
| L1BOH2-8217 | GWB hang ceilings and at heat pumps | 10 | 0 | 05-Jan-15 A | 29-Jan-15 A | |
| L1L-8222 | Complete HVAC drops @ ceilings | 5 | 0 | 05-Jan-15 A | 23-Jan-15 A | |
| L1L-8224 | Complete fire sprinkler drops @ ceilings | 5 | 0 | 05-Jan-15 A | 08-Jan-15 A | |
| L1L-8254 | Complete electrical rough-in at walls | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| I-5350 | Fabricate & install new hydraulic ram | 30 | 0 | 05-Jan-15 A | 29-Jan-15 A | |
| I-7800 | Procure light poles and replacement luminaires | 40 | 14 | 05-Jan-15 A | 05-Jun-15 | 19 |
| LL1-8120 | Complete GWB tape & finish in corridors | 7 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| L1K-8108 | Complete kitchen hood installation and fire blanket wi | 10 | 0 | 05-Jan-15 A | 05-Feb-15 A | |
| L1K-8110 | Complete MEP rough-in above ceiling | 10 | 0 | 05-Jan-15 A | 05-Feb-15 A | |
| L1B-8122 | Framing, complete ceiling at corridors | 5 | 0 | 05-Jan-15 A | 13-Jan-15 A | |

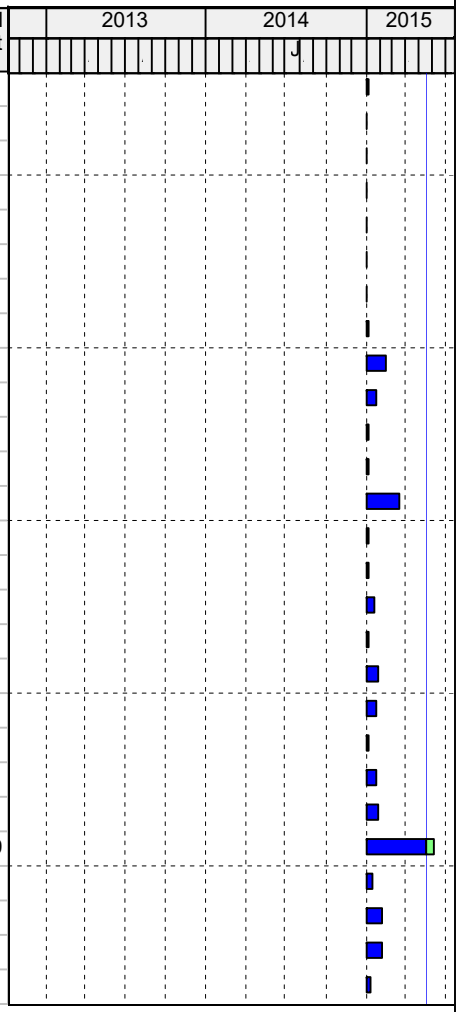



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-5102 | Bar lighting layout - resolve conflicts (RFI) | 7 | 0 | 05-Jan-15 A | 19-Jan-15 A | |
| I-5110 | Bar radius ceiling - resolve framing issues | 5 | 0 | 05-Jan-15 A | 14-Jan-15 A | |
| I-5120 | Dining feature wall - resolve design issues | 7 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| L02-8178 | Complete heat pump enclosures | 5 | 0 | 05-Jan-15 A | 12-Jan-15 A | |
| I-5850 | Owner provide revised lighting layout | 10 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| I-5130 | Bar plumbing relocation - resolve conflicts | 25 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| I-5140 | Damper at BPF #8 - resolve conflicts | 30 | 0 | 05-Jan-15 A | 29-Jan-15 A | |
| I-5150 | Sprinkler pipe furring - resolve conflicts | 15 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| I-5160 | ASI 63 electrical revisions - resolve conflicts | 10 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| L15-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 06-Jan-15 A | 07-Jan-15 A | |
| L07-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L08-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L09-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L10-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L09-7136 | Install Door and Hardware | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L10-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L11-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L12-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L15-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 06-Jan-15 A | 07-Jan-15 A | |
| L11-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 06-Jan-15 A | 12-Jan-15 A | |
| L03-8660 | GWB hang ceilings at Pool | 3 | 0 | 06-Jan-15 A | 04-Feb-15 A | |
| L1K-6011 | Complete HVAC RI @ ceilings | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L1K-6013 | Complete electrical rough-in @ ceilings & inspection | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L1K-6015 | Complete fire sprinkler RI @ ceilings | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L12-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L14-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L15-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |

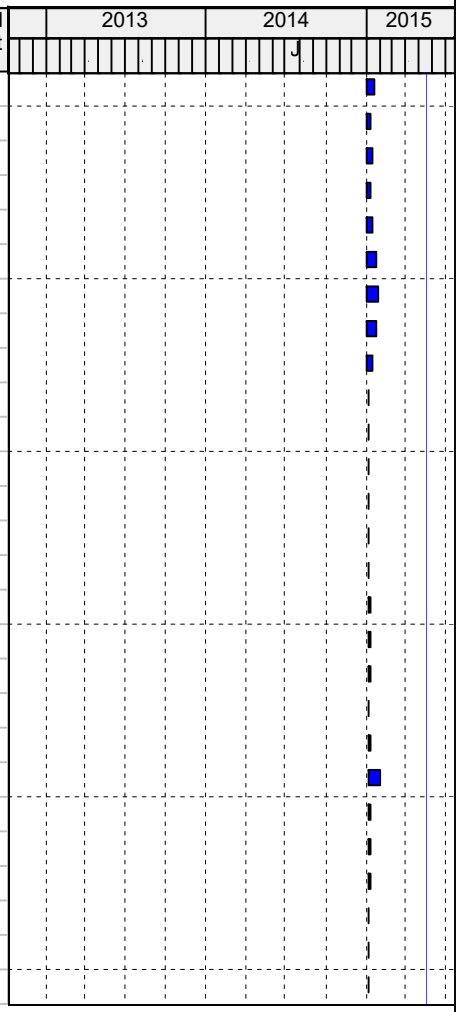



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L15-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 07-Jan-15 A | 20-Jan-15 A | |
| L12-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 07-Jan-15 A | 13-Jan-15 A | |
| CO-7242 | Cx - Heat Pump Start-Up - Levels 5 & 6 | 5 | 0 | 07-Jan-15 A | 09-Jan-15 A | |
| CO-7252 | Cx - Start-Up - FSD & SD Operation Verification | 10 | 0 | 07-Jan-15 A | 22-Jan-15 A | |
| MPP-1026 | Complete Elevation 7/8 (east elevation) | 5 | 0 | 07-Jan-15 A | 16-Feb-15 A | |
| ASI61 | ASI No. 61 - VHP-1 Ductwork Change at Elevator 5 L | 0 | 0 | 07-Jan-15 A | | |
| I-5056 | RFI 832.1 - South Elevation Emergency Exit with Sid | 1 | 0 | 07-Jan-15 A | 14-Jan-15 A | |
| LL1-6014Ib2 | L1 bar redesign - GWB hang, tape, finish (including ir | 12 | 0 | 08-Jan-15 A | 30-Jan-15 A | |
| SW-2310 | Zone 3 - Install irrigation sleeves | 2 | 0 | 08-Jan-15 A | 08-Jan-15 A | |
| I-1638 | Manlift finishes - ceiling grid | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| L03-8662 | GWB tape & finish walls & ceilings at Pool | 7 | 0 | 08-Jan-15 A | 25-Feb-15 A | |
| MPT-1072 | Tower Sign, West (El, 52) | 5 | 0 | 08-Jan-15 A | 14-Apr-15 A | |
| L1L-8220 | Complete fire sprinkler RI @ ceilings | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| L1L-8270 | Complete HVAC RI @ ceilings | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| SW-2224 | Zone 2 - Adjust Comcast vault lids | 2 | 0 | 08-Jan-15 A | 08-Jan-15 A | |
| I-1212 | Resolve stud/duct conflict at east wall | 5 | 0 | 08-Jan-15 A | 14-Jan-15 A | |
| L04-8218 | Install base at corridors (& approve mockup) | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| GB410-100 | Complete GWB - Levels 4-10 | 5 | 0 | 08-Jan-15 A | 14-Jan-15 A | |
| LL1-6014Ib4 | L1 bar redesign - complete reframing | 5 | 0 | 08-Jan-15 A | 15-Jan-15 A | |
| I-5306 | Heat Pump Revision - complete reframing | 5 | 0 | 08-Jan-15 A | 19-Jan-15 A | |
| ASI63 | ASI No. 63 - Mech (Rev. 20), Plumbing (Rev. 18) and | 0 | 0 | 09-Jan-15 A | | |
| L15-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L16-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8121 | Install Bathroom "Barn Doors" | 3 | 0 | 12-Jan-15 A | 26-Mar-15 A | |
| L04-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |

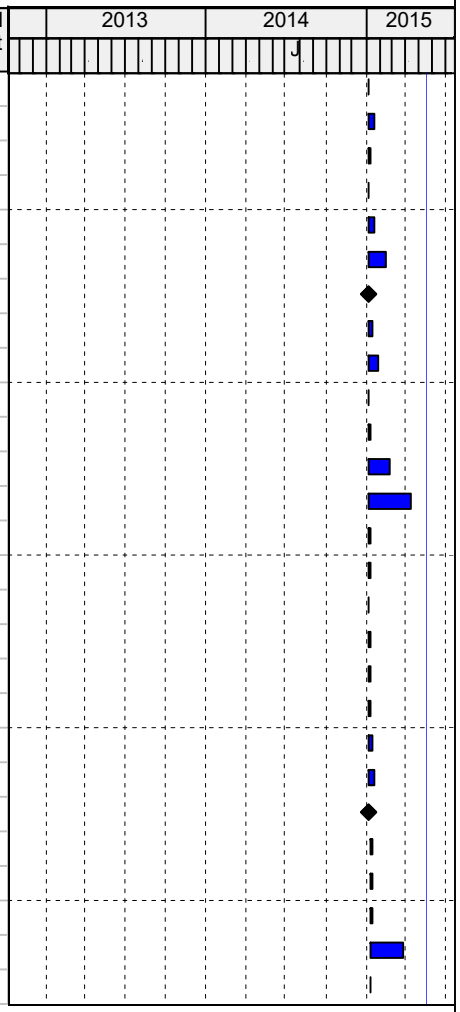



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L06-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L07-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L08-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L09-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L10-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L11-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L12-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L14-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L15-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L11-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L14-7136 | Install doors & hardware | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L14-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L15-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L15-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L14-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L11-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L03-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 12-Jan-15 A | 19-Jan-15 A | |
| CO-7244 | Cx - Heat Pump Start-Up - Levels 7 & 8 | 5 | 0 | 12-Jan-15 A | 14-Jan-15 A | |
| MPT-1068 | Tower Sign, North (El. 51) | 5 | 0 | 12-Jan-15 A | 10-Mar-15 A | |
| L03-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L11-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L14-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L15-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |

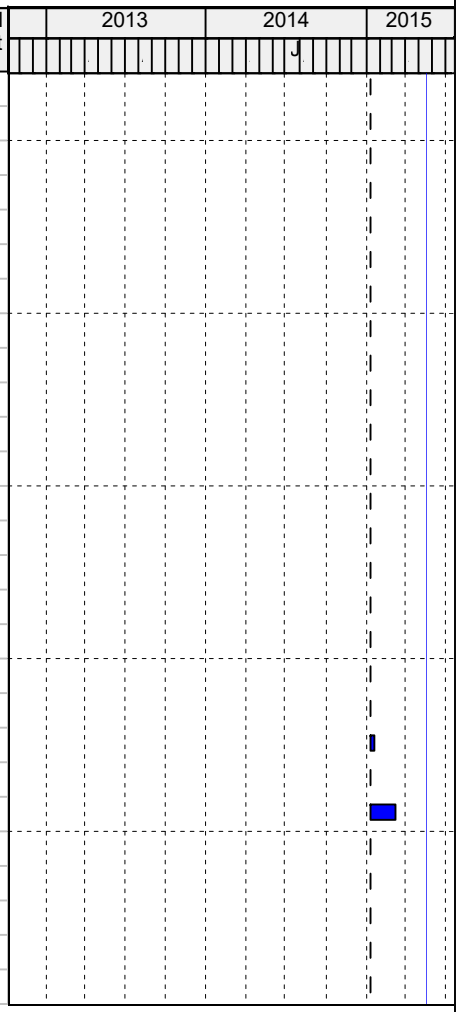



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8144 | GWB hang at Locker Rooms | 2 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| SW-2326 | Zone 3 - Install j-boxes | 3 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| I-5800 | Mechanical correction notice - interference with light t | 10 | 0 | 12-Jan-15 A | 13-Feb-15 A | |
| I-5602 | Frame FCC ceiling | 2 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| CO-7166 | Replace exhaust fitting | 10 | 0 | 12-Jan-15 A | 28-Jan-15 A | |
| MPP-1034 | Deliver Elevation 48 corner panels | 25 | 0 | 12-Jan-15 A | 27-Feb-15 A | |
| MPP-1042 | Deliver Elevation 32 corner panels | 25 | 0 | 12-Jan-15 A | 02-Feb-15 A | |
| MPP-1066 | Deliver Elevation 33/34 corner panels | 25 | 0 | 12-Jan-15 A | 27-Feb-15 A | |
| MPP-1068 | Deliver Elevation 32 spandrel panel head/sill flashings | 25 | 0 | 12-Jan-15 A | 13-Feb-15 A | |
| MPP-1070 | Deliver Elevation 44 spandrel panel head/sill flashings | 25 | 0 | 12-Jan-15 A | 13-Feb-15 A | |
| MPP-1072 | Deliver remaining Elevation 4 panels | 25 | 0 | 12-Jan-15 A | 06-Feb-15 A | |
| MPP-1074 | Deliver remaining Elevation 7 panels | 25 | 0 | 12-Jan-15 A | 06-Feb-15 A | |
| MPP-1076 | Deliver Pool cornice panels | 25 | 0 | 12-Jan-15 A | 23-Mar-15 A | |
| ASI64 | ASI No. 64 - Updated Public Space Carpet Specificat | 0 | 0 | 12-Jan-15 A | | |
| L15-7136 | Install doors & hardware | 1 | 0 | 13-Jan-15 A | 16-Feb-15 A | |
| L03-8664 | Paint, prime & first coat finish at Pool | 3 | 0 | 13-Jan-15 A | 23-Mar-15 A | |
| MPP-1022 | (A) Complete Elevation 40 (pool south elevation, L3-L | 5 | 0 | 13-Jan-15 A | 20-Jan-15 A | |
| L05-8226 | Install base at corridors | 1 | 0 | 13-Jan-15 A | 13-Jan-15 A | |
| L16-8138 | Bathrooms - Install toilet accessories | 2 | 0 | 14-Jan-15 A | 15-Jan-15 A | |
| L14-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| CO-7246 | Cx - Heat Pump Start-Up - Levels 9 & 10 | 5 | 0 | 14-Jan-15 A | 16-Jan-15 A | |
| I-5604 | GWB hang, tape & finish FCC ceiling | 5 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| I-5076 | RFI 860.1 - Southeast Elevation Conflict | 1 | 0 | 14-Jan-15 A | 17-Mar-15 A | |
| I-5078 | RFI 884 - Pedestrian Light Pole Base and Drain Conf | 1 | 0 | 14-Jan-15 A | 28-Jan-15 A | |
| L14-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 15-Jan-15 A | 16-Jan-15 A | |
| L16-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 15-Jan-15 A | 21-Jan-15 A | |
| SW-2126 | Zone 1 - Remove temporary transformer | 5 | 0 | 15-Jan-15 A | 28-Jan-15 A | |

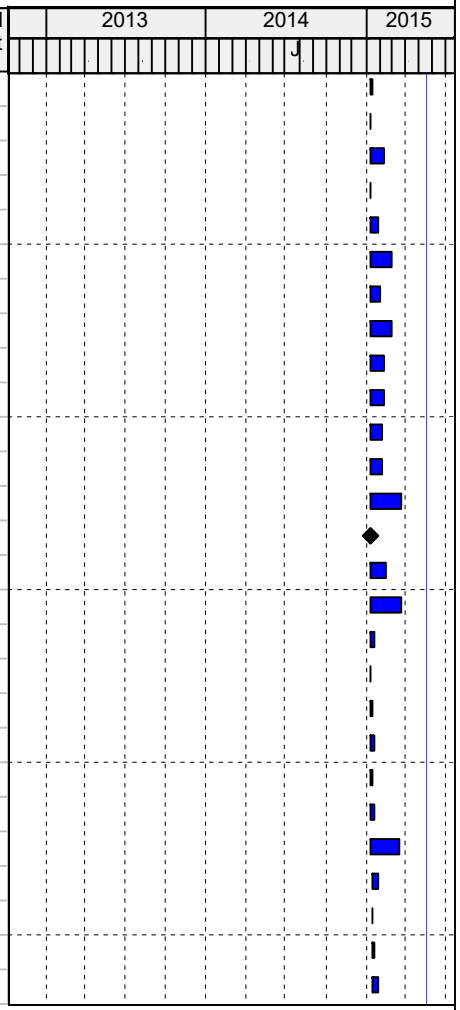



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-5112 | Bar radius ceiling - complete framing | 5 | 0 | 15-Jan-15 A | 20-Jan-15 A | |
| I-5080 | RFI 889 - Site Channelization Plan | 1 | 0 | 15-Jan-15 A | 11-Mar-15 A | |
| L07-8226 | Install base at corridors | 1 | 0 | 16-Jan-15 A | 16-Jan-15 A | |
| I-5060 | RFI 834.1 - NE Retaining Wall Design Clarifications - ( | 1 | 0 | 16-Jan-15 A | 02-Feb-15 A | |
| L16-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| CO-7248 | Cx - Heat Pump Start-Up - Levels 11 & 12 | 5 | 0 | 19-Jan-15 A | 21-Jan-15 A | |
| CO-7254 | Cx - Start-Up - MUA AAON (8) | 5 | 0 | 19-Jan-15 A | 20-Feb-15 A | |
| SW-2020 | Porte Cochere - EIFS at ceiling | 7 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L02-8146 | GWB tape & finish at Locker Rooms | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L1K-8138 | Complete GWB hang & tape | 9 | 0 | 19-Jan-15 A | 06-Feb-15 A | |
| L1L-8252 | Complete electrical/fire alarm rough-in @ ceilings | 3 | 0 | 19-Jan-15 A | 26-Jan-15 A | |
| LL1-8122 | Paint corridors | 6 | 0 | 19-Jan-15 A | 21-Jan-15 A | |
| L1B-6027 | Framing, ceiling at East Ballroom | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L09-8226 | Install base at corridors | 1 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| GB410-102 | Complete painting - Levels 4-10 | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL1-Z2-8110 | Paint, prime & first coat finish at Meeting Rooms | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| I-5122 | Dining feature wall - complete framing | 3 | 0 | 19-Jan-15 A | 21-Jan-15 A | |
| I-5162 | ASI 63 electrical revisions - demo existing | 1 | 0 | 19-Jan-15 A | 19-Jan-15 A | |
| L1B-8170 | Complete cover inspections | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L17-8138 | Bathrooms - Install toilet accessories | 2 | 0 | 20-Jan-15 A | 31-Mar-15 A | |
| MPP-1014 | Caulking - Elevation 1/2/A/B/C/23/24/25 (west elevati | 9 | 0 | 20-Jan-15 A | 30-Jan-15 A | |
| CO-7232 | Cx - TAB - CW Pump Totalization | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| L03-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| LL1-8202 | HVAC trim at ceiling | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| LL1-8206 | Lighting & electrical trim | 4 | 0 | 20-Jan-15 A | 28-Jan-15 A | |
| LL1-8208 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| LL1-Z2-8138 | Paint corridors | 3 | 0 | 20-Jan-15 A | 04-Feb-15 A | |

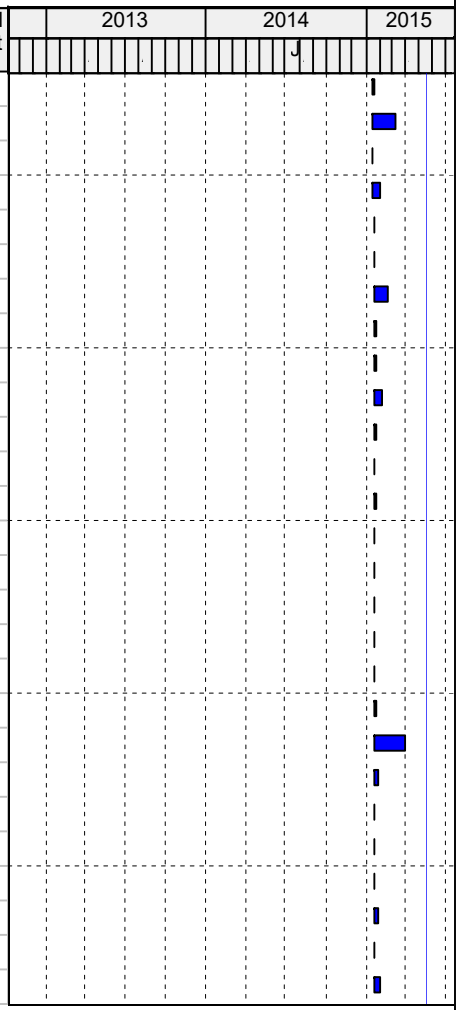



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8226 | Install base at corridors | 1 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| GB410-106 | Complete flooring - Levels 4-10 | 3 | 0 | 20-Jan-15 A | 26-Jan-15 A | |
| L04-8422 | Floor prep | 1 | 0 | 20-Jan-15 A | 02-Feb-15 A | |
| I-5606 | Paint FCC ceiling | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| I-5104 | Bar lighting layout - complete elecrical rough-in | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| I-5164 | ASI 63 electrical revisions - revise electrical | 3 | 0 | 20-Jan-15 A | 02-Feb-15 A | |
| L16-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| CO-7234 | Cx - TAB - CW Water Balancing | 10 | 0 | 21-Jan-15 A | 06-Mar-15 A | |
| L15-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L14-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L12-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L11-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L16-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| CO-7250 | Cx - Heat Pump Start-Up - Levels 14 & 15 | 5 | 0 | 21-Jan-15 A | 23-Jan-15 A | |
| L16-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| I-5304 | Heat Pump Revision - rework GWB | 9 | 0 | 21-Jan-15 A | 30-Jan-15 A | |
| L03-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L04-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L05-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L06-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L07-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L08-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L09-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L11-8226 | Install base at corridors | 1 | 0 | 21-Jan-15 A | 22-Jan-15 A | |
| L05-8422 | Floor prep | 1 | 0 | 21-Jan-15 A | 02-Feb-15 A | |
| ASI65 | ASI No. 65 - Framing Revisions at Foyer 101 | 0 | 0 | 21-Jan-15 A | | |
| L07-7134 | Flooring - VCT | 1 | 0 | 22-Jan-15 A | 22-Jan-15 A | |

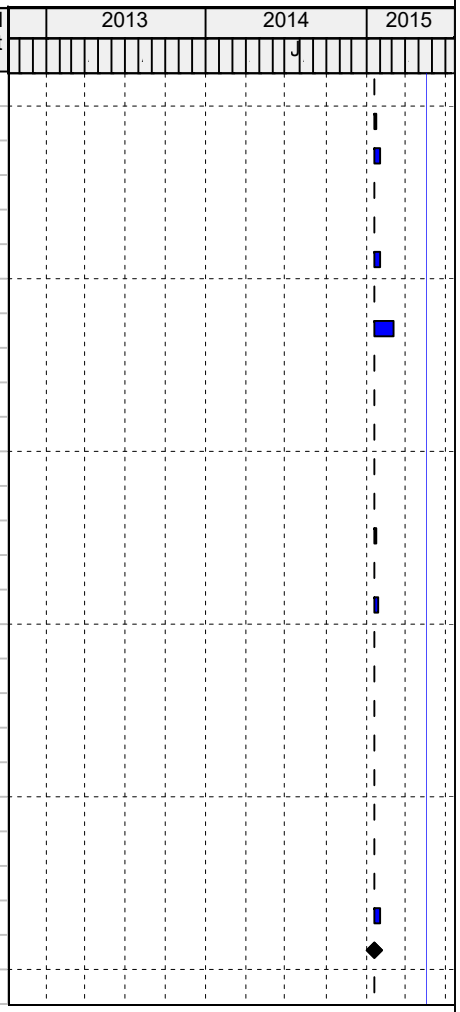



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 22-Jan-15 A | 27-Jan-15 A | |
| LL1-8210 | Fire sprinkler trim | 1 | 0 | 22-Jan-15 A | 22-Jan-15 A | |
| L12-8226 | Install base at corridors | 1 | 0 | 22-Jan-15 A | 23-Jan-15 A | |
| L05-7134 | Flooring - VCT | 1 | 0 | 23-Jan-15 A | 23-Jan-15 A | |
| MPP-1016 | Caulking - Elevation 7/8 (east elevation) | 8 | 0 | 23-Jan-15 A | 24-Feb-15 A | |
| LL1-Z2-8120 | GWB hang, tape & finish ceiling clouds at Jr. Ballroon | 7 | 0 | 23-Jan-15 A | 17-Feb-15 A | |
| LL1-Z3-8148 | Paint Restrooms | 3 | 0 | 23-Jan-15 A | 26-Jan-15 A | |
| MPT-1104 | (B) Install alcoves, east (Elev. 7/8) | 2 | 0 | 23-Jan-15 A | 09-Feb-15 A | |
| L06-8422 | Floor prep | 1 | 0 | 23-Jan-15 A | 23-Jan-15 A | |
| L17-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L06-7134 | Flooring - VCT | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| CO-7216 | Cx - Start-Up Fluid Cooler (power, pre-start & start) | 3 | 0 | 26-Jan-15 A | 28-Jan-15 A | |
| L16-8140 | Install window sills | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| L04-8224 | HVAC grilles & registers at corridors | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| MPT-1058 | Elevation 32 hat channel (south elevation, east of ma | 3 | 0 | 26-Jan-15 A | 17-Feb-15 A | |
| MPT-1090 | Caulking - Elevation 40 (pool south elevation, L3-L17 | 9 | 0 | 26-Jan-15 A | 05-Feb-15 A | |
| LL1-8123 | Floor prep | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| SW-2052 | Zone 4 - Waterproof NW planter walls | 4 | 0 | 26-Jan-15 A | 29-Jan-15 A | |
| L1L-8290 | GWB, top rock | 3 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L10-8131 | Bathrooms - Install access panels | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| L14-8226 | Install base at corridors | 1 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| I-5372 | (S) Elevation 32, complete insulation | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| GB1117-100 | Complete GWB - Levels 3, 11-16 | 7 | 0 | 26-Jan-15 A | 30-Jan-15 A | |
| SW-2322 | Zone 3 - FRP landscape curb at exit door | 5 | 0 | 26-Jan-15 A | 30-Jan-15 A | |
| I-6010 | RFI 901 - Pool topping slab issue (Owner procure floc | 10 | 5 | 26-Jan-15 A | 22-May-15 | 0 |
| L03-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L16-7034 | Install doors & hardware (x42) | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |

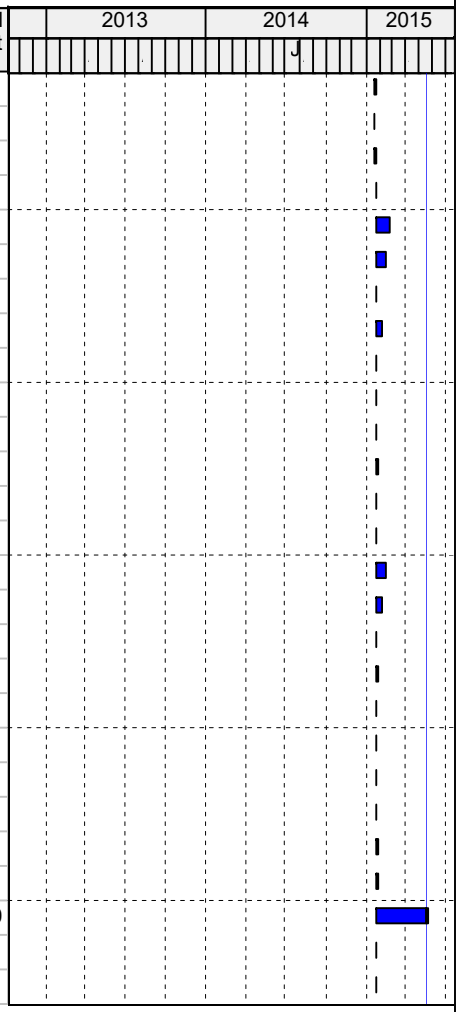



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7034 | Install doors & hardware (x42) | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L08-7134 | Flooring - VCT | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L16-7138 | Electrical trim & finish | 1 | 0 | 27-Jan-15 A | 18-Feb-15 A | |
| L17-7136 | Install doors & hardware | 1 | 0 | 27-Jan-15 A | 17-Feb-15 A | |
| I-1640 | Manlift finishes - Install window sills | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L03-8668 | Remove scaffolding at pool pit | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L17-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L11-8131 | Bathrooms - Install access panels | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L15-8226 | Install base at corridors | 1 | 0 | 27-Jan-15 A | 28-Jan-15 A | |
| MPP-1052 | (B) Elevation 3 (south elevation, west of manlift, L1-L: | 5 | 0 | 27-Jan-15 A | 30-Jan-15 A | |
| GB410-108 | Complete base - Levels 4-10 | 4 | 0 | 27-Jan-15 A | 30-Jan-15 A | |
| L08-8422 | Floor prep | 1 | 0 | 27-Jan-15 A | 28-Jan-15 A | |
| I-5132 | Bar plumbing relocation - relocate waste line | 3 | 0 | 27-Jan-15 A | 29-Jan-15 A | |
| I-5152 | Sprinkler pipe furring - install framing around pipe | 2 | 0 | 27-Jan-15 A | 28-Jan-15 A | |
| L09-7134 | Flooring - VCT | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L17-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L17-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| EL-6042 | Elev 6 - Install EMR heat pump | 6 | 0 | 28-Jan-15 A | 25-Feb-15 A | |
| MPT-1056 | Complete Elevation 31 (above L12 terrace, west elev | 3 | 0 | 28-Jan-15 A | 13-Feb-15 A | |
| L1L-8256 | GWB hang walls | 3 | 0 | 28-Jan-15 A | 05-Feb-15 A | |
| SW-2230 | Zone 2 - Repair sidewalk north of 3rd Ave | 5 | 0 | 28-Jan-15 A | 30-Jan-15 A | |
| L12-8131 | Bathrooms - Install access panels | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L08-8226 | Install base at corridors | 1 | 0 | 28-Jan-15 A | 30-Jan-15 A | |
| L16-8226 | Install base at corridors | 1 | 0 | 28-Jan-15 A | 29-Jan-15 A | |
| I-5373 | (S) Elevation 32, install sign backing | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L07-8422 | Floor prep | 1 | 0 | 28-Jan-15 A | 03-Feb-15 A | |
| I-6000 | Resolve cloud framing engineering issue | 5 | 0 | 28-Jan-15 A | 03-Feb-15 A | |

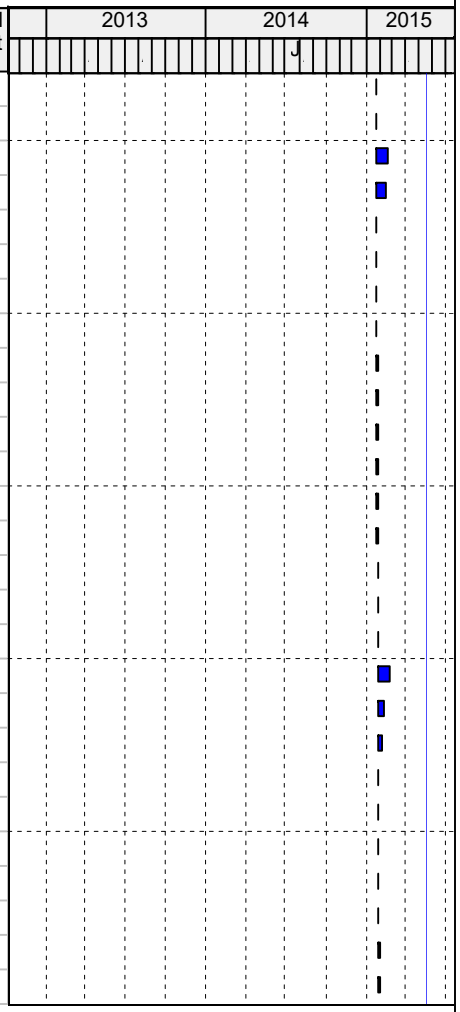



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-7134 | Flooring - VCT | 1 | 0 | 29-Jan-15 A | 29-Jan-15 A | |
| L1L-8226 | GWB hang ceilings & complete walls | 3 | 0 | 29-Jan-15 A | 23-Feb-15 A | |
| L1L-8248 | Complete electrical/fire alarm rough-in @ ceilings | 3 | 0 | 29-Jan-15 A | 02-Feb-15 A | |
| L1L-8250 | Complete HVAC RI @ ceilings | 5 | 0 | 29-Jan-15 A | 04-Feb-15 A | |
| L03-8218 | Install base at corridors | 1 | 0 | 29-Jan-15 A | 30-Jan-15 A | |
| MPP-1062 | (C) Install level 3 cornice metal (Porte Cochere) | 2 | 0 | 29-Jan-15 A | 04-Feb-15 A | |
| EL-6040 | Elev 6 - Install machine room controller equipment/hy | 3 | 0 | 30-Jan-15 A | 24-Feb-15 A | |
| EL-6054 | Elev 6 - Install EMR doors, hardware & labeling | 2 | 0 | 30-Jan-15 A | 23-Feb-15 A | |
| LL1-8160 | Flooring - carpet | 10 | 0 | 30-Jan-15 A | 18-Feb-15 A | |
| I-5472 | Reframe Laundry Room ceiling (per ceiling height RF | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5474 | Restore Laundry Room GWB (hang & tape) (per ceili | 5 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5476 | Repaint Laundry Room ceiling | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5478 | Demo existing Laundry Room ceiling | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5480 | Revise MEP above Laundry Room ceiling | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5134 | Bar plumbing relocation - adust framing | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5136 | Bar plumbing relocation - GWB hang, tape & finish [D | 7 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5138 | Bar plumbing relocation - paint [DELETED] | 2 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5142 | Damper at BPF #8 - mechanical revisions | 2 | 0 | 30-Jan-15 A | 02-Feb-15 A | |
| L04-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 02-Feb-15 A | 02-Feb-15 A | |
| L04-7134 | Flooring - VCT | 1 | 0 | 02-Feb-15 A | 02-Feb-15 A | |
| LL1-8124a | Install base | 10 | 0 | 02-Feb-15 A | 23-Feb-15 A | |
| CO-7218 | Cx - Heat Pump Start-Up - Levels 16 & 17 | 5 | 0 | 02-Feb-15 A | 04-Feb-15 A | |
| LL1-6014Id | L1 bar redesign - paint ceilings at Excercise & MR9 | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| EL-1236 | Elev 1&2 - Walsh/TKE pre-inspection | 6 | 0 | 02-Feb-15 A | 27-Feb-15 A | |
| MPT-1050 | (B) Install louvers, east | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| MPT-1070 | Tower Sign, East (El. 44) | 5 | 0 | 02-Feb-15 A | 10-Feb-15 A | |
| L1L-8272 | GWB hang ceilings | 3 | 0 | 02-Feb-15 A | 04-Feb-15 A | |

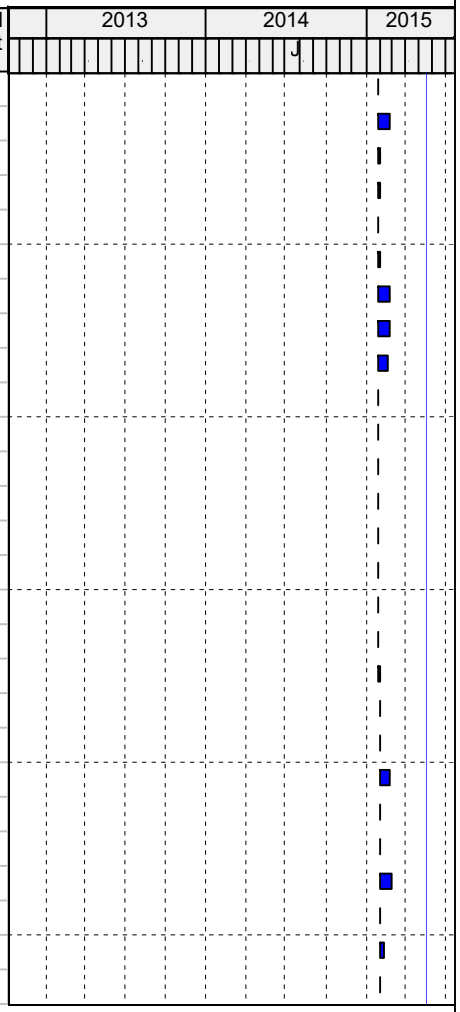



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2320 | Zone 3 - Pour ped pole base | 3 | 0 | 02-Feb-15 A | 05-Feb-15 A | |
| LL1-8156 | Install doors & hardware at corridors | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| L1B-6015 | HVAC drops at West Ballrooms | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L1B-6021 | Electrical drops at West Ballrooms | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L1B-6029 | HVAC drops at East Ballroom | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L1B-6031 | Electrical drops at East Ballroom | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L06-8226 | Install base at corridors | 1 | 0 | 02-Feb-15 A | 02-Feb-15 A | |
| GB410-104 | Complete vinyl wallcoverings - Levels 4-10 | 4 | 0 | 02-Feb-15 A | 17-Feb-15 A | |
| GB1117-102 | Complete painting - Levels 3, 11-16 | 3 | 0 | 02-Feb-15 A | 04-Feb-15 A | |
| SW-2234 | Zone 2 - FRP door curbs | 4 | 0 | 02-Feb-15 A | 05-Feb-15 A | |
| I-6950 | Resolve MEP/ceiling height conflicts | 1 | 0 | 02-Feb-15 A | 13-Mar-15 A | |
| L05-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L04-7138 | Electrical trim & finish | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L05-7138 | Electrical trim & finish | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L11-7134 | Flooring - VCT | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| SW-2022 | Zone 4 - Remove pedestrian protection on 110th Ave | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L1L-8246 | Complete fire sprinkler RI @ ceilings | 2 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| LL1-8184 | Install storefront at Exercise Room | 1 | 0 | 03-Feb-15 A | 02-Mar-15 A | |
| L12-8422 | Floor prep | 1 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| L14-8422 | Floor prep | 1 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| L15-8422 | Floor prep | 1 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| I-5144 | Damper at BPF #8 - framing revisions | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| I-5154 | Sprinkler pipe furring - GWB hang | 7 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| I-5166 | ASI 63 electrical revisions - insulation | 2 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| ASI62r1 | ASI No. 62 (Revised) - Civil Site Grading Revisions an | 0 | 0 | 03-Feb-15 A | | |
| L06-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 04-Feb-15 A | 04-Feb-15 A | |
| L12-7134 | Flooring - VCT | 1 | 0 | 04-Feb-15 A | 04-Feb-15 A | |

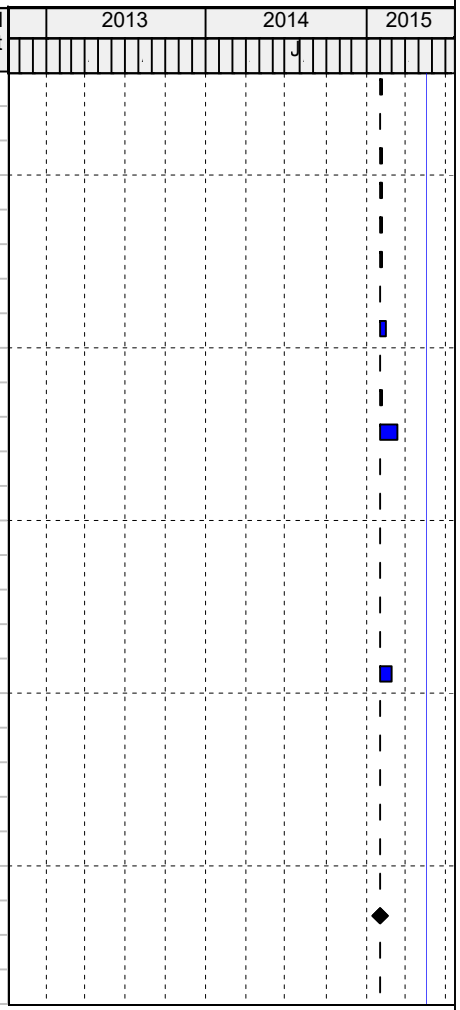



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8142 | Ceramic tile in restrooms | 7 | 0 | 04-Feb-15 A | 20-Feb-15 A | |
| L1K-8144 | Paint, prime & first coat finish | 3 | 0 | 04-Feb-15 A | 09-Mar-15 A | |
| LL1-Z2-8158 | Wall coverings - vinyl at Meeting Rooms | 2 | 0 | 04-Feb-15 A | 05-Feb-15 A | |
| L09-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 06-Feb-15 A | |
| L10-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 09-Feb-15 A | |
| L11-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 09-Feb-15 A | |
| L16-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 10-Feb-15 A | |
| I-5146 | Damper at BPF #8 - complete GWB hang | 1 | 0 | 04-Feb-15 A | 04-Feb-15 A | |
| I-5168 | ASI 63 electrical revisions - vapor barrier | 2 | 0 | 04-Feb-15 A | 05-Feb-15 A | |
| L07-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 05-Feb-15 A | 05-Feb-15 A | |
| L14-7134 | Flooring - VCT | 1 | 0 | 05-Feb-15 A | 05-Feb-15 A | |
| L1L-8102a | GWB tape & finish walls & ceilings (Dining & Lounge) | 7 | 0 | 05-Feb-15 A | 12-Feb-15 A | |
| LL1-8170 | Flooring - tile at elevator lobby | 3 | 0 | 05-Feb-15 A | 09-Feb-15 A | |
| LL1-8186 | Wall coverings - vinyl at corridors | 5 | 0 | 05-Feb-15 A | 19-Feb-15 A | |
| L1B-6023 | Fire sprinkler drops at West Ballrooms | 5 | 0 | 05-Feb-15 A | 09-Feb-15 A | |
| L1B-6033 | Fire sprinkler drops at East Ballroom | 5 | 0 | 05-Feb-15 A | 09-Feb-15 A | |
| GB1117-106 | Complete flooring - Levels 3, 11-16 | 4 | 0 | 05-Feb-15 A | 10-Feb-15 A | |
| I-6100 | Resolve lighting/access panel conflict | 5 | 0 | 05-Feb-15 A | 13-Feb-15 A | |
| GB1117-104 | Complete vinyl wallcoverings - Levels 3, 11-16 | 5 | 0 | 05-Feb-15 A | 11-Feb-15 A | |
| L08-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 06-Feb-15 A | 06-Feb-15 A | |
| L15-7134 | Flooring - VCT | 1 | 0 | 06-Feb-15 A | 06-Feb-15 A | |
| MPP-1054 | Caulking - Elevation 3 (south elevation, west of manli | 3 | 0 | 06-Feb-15 A | 10-Feb-15 A | |
| ASI66 | ASI No. 66 - MDP Electrical Drawings Revision 23A | 0 | 0 | 06-Feb-15 A | | |
| L03-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L04-8408 | Install base at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L05-8408 | Install base at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L06-8408 | Install base at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |

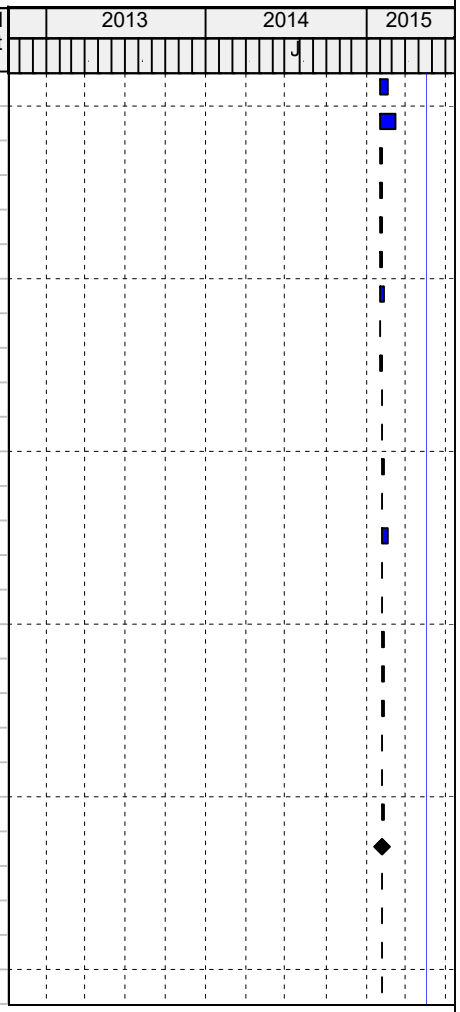



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L16-7134 | Flooring - VCT | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L1K-8102a | GWB hang ceilings at Public Restroom | 2 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| LL2-2094 | Install doors & hardware at Laundry | 2 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| SW-2032 | Zone 4 - Demo existing trees & hardscapes | 3 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| CO-7139 | Install remaining devices & prep devices for testing - | 7 | 0 | 09-Feb-15 A | 03-Mar-15 A | |
| MPP-1024 | (B) Complete Elevation 4 (south elevation, east of tov | 2 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| L1L-8218 | Frame ceilings & inspection | 5 | 0 | 09-Feb-15 A | 12-Feb-15 A | |
| L1K-8136 | Ceiling grid & inspection | 4 | 0 | 09-Feb-15 A | 11-Feb-15 A | |
| L1L-8274 | GWB tape & finish walls & ceilings | 7 | 0 | 09-Feb-15 A | 24-Feb-15 A | |
| L15-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L16-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L17-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L14-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| I-5170 | ASI 63 electrical revisions - GWB hang, tape & finish | 7 | 0 | 09-Feb-15 A | 17-Feb-15 A | |
| SW-2058 | Zone 4 - Demo existing curb at 110th | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| MPT-1114 | Cap metal - Porte Cochere | 3 | 0 | 09-Feb-15 A | 12-Feb-15 A | |
| I-5172 | Resolve Bar Area RFIs & complete revised work | 10 | 0 | 09-Feb-15 A | 04-Mar-15 A | |
| I-2960 | Lack of Stainless Steel Ceiling Closure Pieces (Shrou | 5 | 0 | 09-Feb-15 A | 13-Mar-15 A | |
| L07-8408 | Install base at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L08-8408 | Install base at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L09-8408 | Install base at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L10-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L11-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L17-7134 | Flooring - VCT | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L09-8224 | HVAC grilles & registers at corridors | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L08-8224 | HVAC grilles & registers at corridors | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |

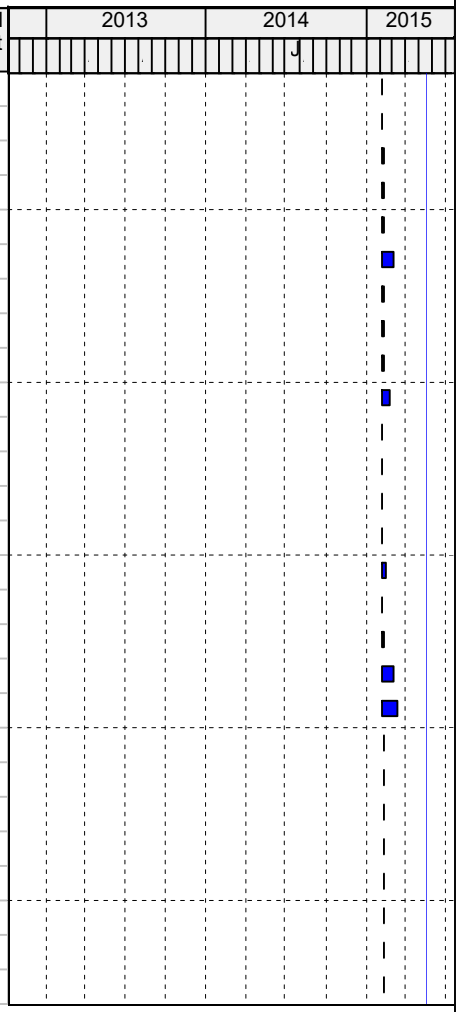



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-8224 | HVAC grilles & registers at corridors | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| SW-2036 | Zone 4 - Grade for curb and gutter | 2 | 0 | 10-Feb-15 A | 11-Feb-15 A | |
| CO-7140 | Fire Alarm System Device Testing - Tower Levels 4 thr | 7 | 0 | 10-Feb-15 A | 05-Mar-15 A | |
| L17-8422 | Floor prep | 1 | 0 | 10-Feb-15 A | 11-Feb-15 A | |
| MPT-1116 | Cap metal - Pool high roof | 3 | 0 | 10-Feb-15 A | 12-Feb-15 A | |
| ASI67 | ASI No. 67 - Meeting Room Door Hardware Revisions | 0 | 0 | 10-Feb-15 A | | |
| L10-8408 | Install base at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L11-8408 | Install base at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L12-8408 | Install base at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L12-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L14-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L03-7134 | Flooring - VCT | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| MPT-1018a | Install hi-roof cornice metal | 8 | 0 | 11-Feb-15 A | 08-Apr-15 A | |
| SW-2038 | Zone 4 - FRP curb & gutter | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| SW-2046 | Zone 4 - Install conduit | 2 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L1K-8152 | Install doors & hardware | 3 | 0 | 11-Feb-15 A | 17-Feb-15 A | |
| L1L-8228 | GWB tape & finish | 7 | 0 | 11-Feb-15 A | 03-Mar-15 A | |
| SW-2054 | Zone 4 - Install flag pole bases | 3 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| L17-8226 | Install base at corridors | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| MPP-1058 | (B) Install podium cornice, south/east | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| L03-8422 | Floor prep | 1 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| MPT-1108 | Cap metal - complete at tower | 5 | 0 | 11-Feb-15 A | 13-Feb-15 A | |
| MPT-1112 | Cap metal - complete at Ballroom roof | 3 | 0 | 11-Feb-15 A | 13-Feb-15 A | |
| CO-7404 | Cx - FPT - Heat Pumps | 3 | 0 | 11-Feb-15 A | 13-Feb-15 A | |
| L14-8408 | Install base at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L15-8408 | Install base at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L15-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |

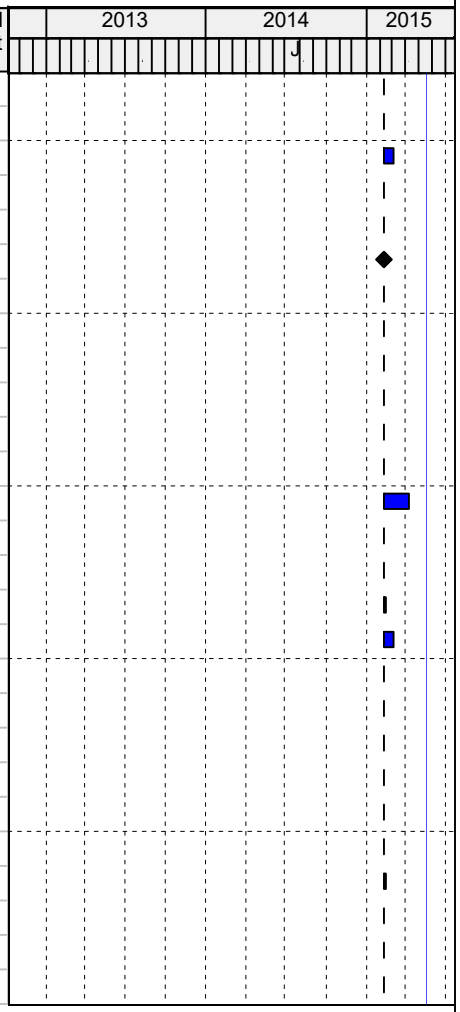



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-8408 | Install base at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L16-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L06-7138 | Electrical trim & finish | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L1K-8102b | GWB tape & finish at Restrooms | 7 | 0 | 12-Feb-15 A | 25-Feb-15 A | |
| LL1-8154 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 12-Feb-15 A | 20-Feb-15 A | |
| ASI68 | ASI No. 68 - MDP Mechanical Drawings Revision 21 | 0 | 0 | 12-Feb-15 A | | |
| LL1-Z3-FCC28 | Electrical trim & finish at FCC | 4 | 0 | 12-Feb-15 A | 16-Feb-15 A | |
| LL1-8182 | Install doors & hardware at Exercise Room | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| GB1117-108 | Complete base - Levels 3, 11-16 | 5 | 0 | 12-Feb-15 A | 18-Feb-15 A | |
| GB1117-110 | Complete countertops - Levels 3, 11-16 | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| GB1117-112 | Complete shower/tub surrounds - Levels 3, 11-16 | 3 | 0 | 12-Feb-15 A | 16-Feb-15 A | |
| L17-8408 | Install base at Elevator Lobby | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| L17-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| SW-2118 | Zone 1 - FRP sidewalk (NE corner) | 2 | 0 | 13-Feb-15 A | 13-Mar-15 A | |
| SW-2034 | Zone 4 - Install irrigation sleeves | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| SW-2060 | Zone 4 - Sawcut curb & gutter | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| ASI69 | ASI No. 69 - Architectural Level 1 Revised Ceiling Plai | 0 | 0 | 13-Feb-15 A | | |
| LL1-Z2-8142 | Wall coverings - vinyl at corridors | 3 | 0 | 16-Feb-15 A | 19-Feb-15 A | |
| I-6900 | Resolve Garage EF motor/VFD issue (including corre | 20 | 0 | 16-Feb-15 A | 25-Mar-15 A | |
| I-5066 | RFI 848.1 -Flagpole Lighting - South Light/Flagpole E | 1 | 0 | 16-Feb-15 A | 16-Mar-15 A | |
| L03-7136 | Install doors & hardware | 2 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| MPP-1012 | Caulking - Elevation 4 (south elevation, east of tower) | 6 | 0 | 16-Feb-15 A | 23-Feb-15 A | |
| L10-8224 | HVAC grilles & registers at corridors | 1 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| L06-8224 | HVAC grilles & registers at corridors | 1 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| L05-8224 | HVAC grilles & registers at corridors | 1 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| SW-2040 | Zone 4 - Fine grade for sidewalk and planter curb | 3 | 0 | 16-Feb-15 A | 17-Feb-15 A | |
| MPP-1036 | Podium Signs, East | 5 | 0 | 16-Feb-15 A | 18-Feb-15 A | |

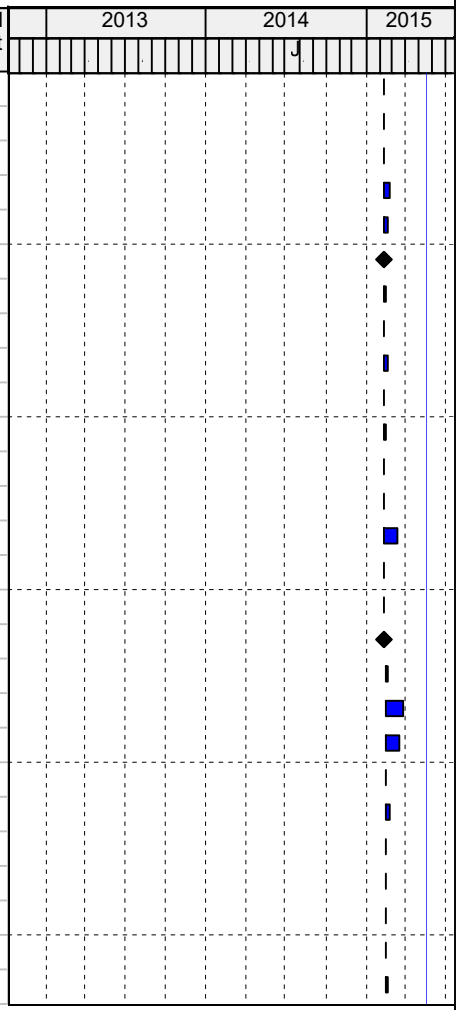



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8150 | HVAC drops/trim at ceiling | 2 | 0 | 16-Feb-15 A | 17-Feb-15 A | |
| LL2-8146 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 16-Feb-15 A | 23-Feb-15 A | |
| LL1-8172 | Ceiling grid & inspection at Exercise Room (additional | 6 | 0 | 16-Feb-15 A | 23-Feb-15 A | |
| L1K-8162 | Complete wallcoverings (FRP) | 2 | 0 | 16-Feb-15 A | 17-Feb-15 A | |
| L1B-6011 | GWB, hang ceiling at West Ballrooms | 4 | 0 | 16-Feb-15 A | 18-Feb-15 A | |
| L1B-8138 | GWB hang, tape & finish ceilings at corridors (comple | 11 | 6 | 16-Feb-15 A | 25-May-15 | -6 |
| LL1-8176 | HVAC drops/trim to grid | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L03-8408 | Install base at Elevator Lobby | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L03-7034 | Install doors & hardware (x42) | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L03-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L07-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L08-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L09-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L10-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L11-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L12-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L16-7136 | Install doors & hardware | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| LL2-2062 | Ceiling grid at Laundry | 4 | 0 | 17-Feb-15 A | 30-Mar-15 A | |
| L15-8224 | HVAC grilles & registers at corridors | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L14-8224 | HVAC grilles & registers at corridors | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| CO-7258 | Cx - Start-Up - KMUA Trane (2) | 2 | 0 | 17-Feb-15 A | 20-Feb-15 A | |
| SW-2044 | Zone 4 - FRP sidewalk (SW corner remaining) | 3 | 0 | 17-Feb-15 A | 02-Apr-15 A | |
| LL1-Z3-FCC30 | Data/phone trim/finish at FCC | 4 | 0 | 17-Feb-15 A | 19-Feb-15 A | |
| LL1-Z3-6036 | GWB hang, tape & finish ceiling at Food Prep (Dry St | 5 | 0 | 17-Feb-15 A | 02-Mar-15 A | |
| MPT-1092 | Caulking - Elevation 31 (above L12 terrace, west elev | 4 | 0 | 17-Feb-15 A | 20-Feb-15 A | |
| MPT-1098 | Caulking - Elevation 30 (south elevation, west of man | 6 | 0 | 17-Feb-15 A | 23-Mar-15 A | |
| LL1-6014Id2 | L1 bar redesign - install wall coverings at MR9 | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |

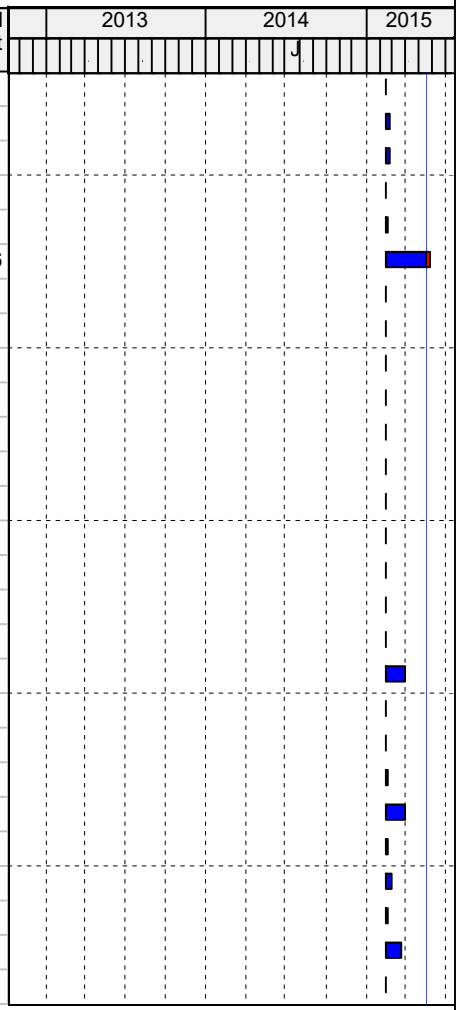



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8146 | Fire sprinkler drops/trim at ceiling | 1 | 0 | 17-Feb-15 A | 10-Mar-15 A | |
| L1K-8148 | Lighting & electrical trim at ceiling | 2 | 0 | 17-Feb-15 A | 10-Mar-15 A | |
| GB1117-114 | Complete plumbing fixture installation - Levels 3, 11-1 | 4 | 0 | 17-Feb-15 A | 20-Feb-15 A | |
| L1K-8164 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 17-Feb-15 A | 10-Mar-15 A | |
| MPT-1062 | Elevation 32 metal panels (south elevation, east of m | 8 | 0 | 18-Feb-15 A | 26-Mar-15 A | |
| L14-7138 | Electrical trim & finish | 1 | 0 | 18-Feb-15 A | 18-Feb-15 A | |
| L15-7138 | Electrical trim & finish | 1 | 0 | 18-Feb-15 A | 18-Feb-15 A | |
| L17-7138 | Electrical trim & finish | 1 | 0 | 18-Feb-15 A | 18-Feb-15 A | |
| CO-7262 | Cx - Start-Up - Electric Unit Heaters | 3 | 0 | 18-Feb-15 A | 30-Mar-15 A | |
| LL1-8174 | Wall coverings - vinyl at Exercise Room | 2 | 0 | 18-Feb-15 A | 19-Feb-15 A | |
| L1B-6017 | GWB, hang ceiling at East Ballrooms | 4 | 0 | 18-Feb-15 A | 20-Feb-15 A | |
| SW-2062 | Zone 4 - Patch curb & gutter | 2 | 0 | 18-Feb-15 A | 19-Feb-15 A | |
| CO-7256 | Cx - Start-Up - Elevator Machine Room Ductless Split | 1 | 0 | 19-Feb-15 A | 19-Feb-15 A | |
| LL1-8178 | Lighting & electrical drops to grid | 2 | 0 | 19-Feb-15 A | 20-Feb-15 A | |
| LL1-8180 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 19-Feb-15 A | 20-Feb-15 A | |
| GB410-110 | Complete countertops - Levels 4-10 | 1 | 0 | 19-Feb-15 A | 19-Feb-15 A | |
| GB410-112 | Complete shower/tub surrounds - Levels 4-10 | 1 | 0 | 19-Feb-15 A | 19-Feb-15 A | |
| GB410-118 | Complete barn doors - Levels 4-10 | 1 | 0 | 19-Feb-15 A | 19-Feb-15 A | |
| GB1117-118 | Complete barn doors - Levels 3, 11-16 | 2 | 0 | 19-Feb-15 A | 20-Feb-15 A | |
| LL1-Z2-8160a | Flooring - carpet at Meeting Rooms | 2 | 0 | 19-Feb-15 A | 23-Feb-15 A | |
| LL2-2098 | HVAC drops to grid at Laundry | 2 | 0 | 20-Feb-15 A | 04-Mar-15 A | |
| LL2-2088 | Lighting & electrical drops to grid at Laundry | 2 | 0 | 20-Feb-15 A | 09-Mar-15 A | |
| L1K-8123 | Floor prep | 2 | 0 | 20-Feb-15 A | 23-Feb-15 A | |
| LL1-8158 | Floor prep at corridors | 2 | 0 | 20-Feb-15 A | 23-Feb-15 A | |
| L1B-8102a | GWB, tape & finish ceiling at West Ballroom | 7 | 0 | 20-Feb-15 A | 02-Mar-15 A | |
| GB410-114 | Complete plumbing fixture installation - Levels 4-10 | 3 | 0 | 20-Feb-15 A | 24-Feb-15 A | |
| LL2-2106 | Floor prep | 1 | 0 | 20-Feb-15 A | 20-Feb-15 A | |

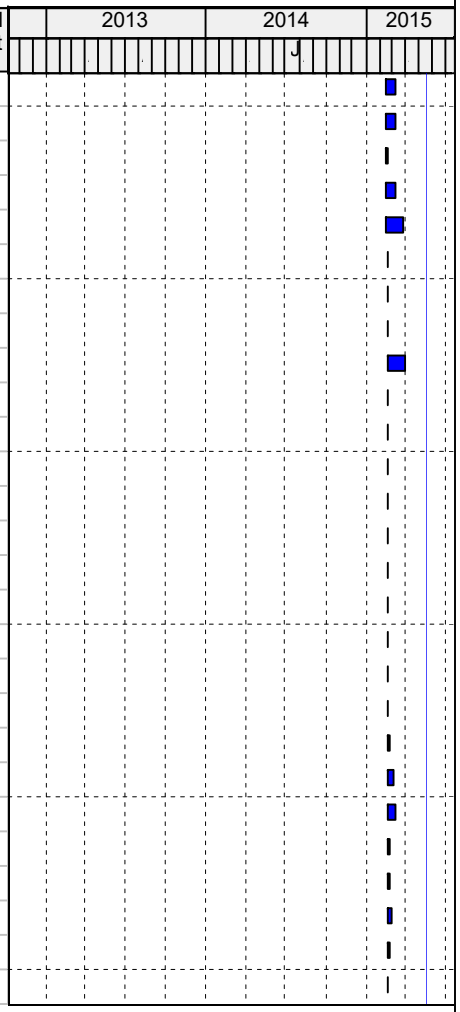



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2086 | Flooring - epoxy remainder of floor (including prep) | 6 | 0 | 21-Feb-15 A | 26-Feb-15 A | |
| MPT-1102 | Elevation 32 spandrel panels (south elevation, east o | 2 | 0 | 21-Feb-15 A | 16-Mar-15 A | |
| LL2-2104 | Flooring - epoxy at equipment alcoves | 5 | 0 | 21-Feb-15 A | 26-Feb-15 A | |
| LL1-Z3-8164 | Field measure & fabricate countertops | 15 | 0 | 21-Feb-15 A | 23-Apr-15 A | |
| LL1-8116f | Fabricate & deliver countertops | 10 | 0 | 21-Feb-15 A | 23-Apr-15 A | |
| LL1-Z2-8118a | Install decorative light fixtures | 3 | 0 | 23-Feb-15 A | 03-Mar-15 A | |
| LL1-Z2-8124a | Install base | 10 | 0 | 23-Feb-15 A | 27-Feb-15 A | |
| CO-7400 | Cx - 3rd Party Cx of Mechanical, Plumbing, Electrical | 40 | 9 | 23-Feb-15 A | 29-May-15 | 8 |
| LL1-Z3-8144 | Install toilets at Restrooms | 4 | 0 | 23-Feb-15 A | 27-Feb-15 A | |
| LL1-8166 | Install base at corridors | 5 | 0 | 23-Feb-15 A | 27-Feb-15 A | |
| LL1-Z2-8122 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 23-Feb-15 A | 09-Mar-15 A | |
| GB1117-116 | Complete shower doors - Levels 3, 11-16 | 2 | 0 | 23-Feb-15 A | 24-Feb-15 A | |
| L17-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| L16-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| L12-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| L11-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| L03-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| MPT-1100 | Install spandrel, east (Elevation 44) | 2 | 0 | 24-Feb-15 A | 26-Feb-15 A | |
| SW-2064 | Porte Cochere - Fill and grade Porte Cochere drive | 3 | 0 | 24-Feb-15 A | 06-Mar-15 A | |
| L1BOH2-8104 | Paint, prime | 2 | 0 | 24-Feb-15 A | 13-Apr-15 A | |
| L1K-8124a | Flooring - epoxy - east end | 5 | 0 | 24-Feb-15 A | 26-Feb-15 A | |
| LL2-8148 | Fire sprinkler drops to grid | 1 | 0 | 24-Feb-15 A | 09-Mar-15 A | |
| LL1-8162 | Flooring - carpet at corridors | 5 | 0 | 24-Feb-15 A | 02-Mar-15 A | |
| LL1-Z2-8128 | HVAC trim at ceiling | 1 | 0 | 24-Feb-15 A | 03-Mar-15 A | |
| LL1-Z2-8130 | Fire sprinkler trim | 1 | 0 | 24-Feb-15 A | 04-Mar-15 A | |
| MPT-1052 | Elevation 48/49 (north elevation, east of 51, L3-L17) | 3 | 0 | 25-Feb-15 A | 11-Mar-15 A | |
| CO-7100T | Cx - Start-Up - Life Safety Exhaust Fans and VFD's | 13 | 0 | 25-Feb-15 A | 03-Apr-15 A | |

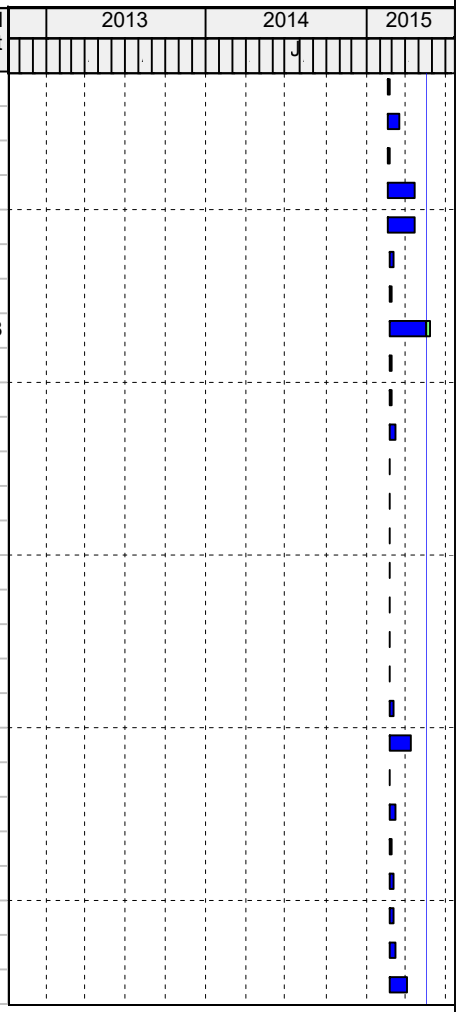



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6044 | Elev 6 - Electrical trim & finish | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| EL-6046 | Elev 6 - Fire alarm trim | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| EL-6048 | Elev 6 - Fire sprinkler trim | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| EL-6050 | Elev 6 - Install pit grates | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| L1L-8276 | Paint, prime & first coat finish | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| GB410-116 | Complete shower doors - Levels 4-10 | 2 | 0 | 25-Feb-15 A | 26-Feb-15 A | |
| L1BOH2-8114 | Ceiling grid & inspection | 4 | 0 | 26-Feb-15 A | 18-Mar-15 A | |
| SW-2066 | Porte Cochere - FRP planter curb | 2 | 0 | 26-Feb-15 A | 27-Feb-15 A | |
| L03-8684 | Pourback piping trench | 1 | 0 | 26-Feb-15 A | 26-Feb-15 A | |
| AS70 | ASI No. 70 - Site Illumination Plan | 0 | 0 | 26-Feb-15 A | | |
| I-5082 | ASI 70 - Site Illumination Plan | 0 | 0 | 26-Feb-15 A | | |
| L1BOH2-8200 | Paint, first coat finish | 1 | 0 | 26-Feb-15 A | 13-Apr-15 A | |
| CO-7220 | Cx - Start-Up - Common Space Heat Pump | 4 | 0 | 26-Feb-15 A | 12-May-15 A | |
| I-3102 | GWB, tape & finish ceiling at East Ballroom | 7 | 0 | 26-Feb-15 A | 06-Mar-15 A | |
| I-5124 | Dining feature wall - install plywood backing | 1 | 0 | 26-Feb-15 A | 26-Feb-15 A | |
| L03-8686 | Cure piping trench | 14 | 0 | 27-Feb-15 A | 12-Mar-15 A | |
| L1L-8114a | Install 9-wood celing supports - south of Grid K | 3 | 0 | 27-Feb-15 A | 04-Mar-15 A | |
| L1K-8124b | Flooring - epoxy - west end (including prep) | 7 | 0 | 27-Feb-15 A | 06-Mar-15 A | |
| CO-7104T | Fire Alarm & Smoke Control Pre-Testing (Tower) - Tow | 3 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7112T | City of Bellevue/3rd Party Fire Sprinkler Inspection / A | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7118T | City of Bellevue/3rd Party Fire Alarm Inspection / Appl | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7106T | City of Bellevue/3rd Party Smoke Control Testing (Tow | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7412 | Cx - Pressure Testing - GC Indicates Podium Complet | 0 | 0 | | 01-Mar-15 A | |
| CO-7416 | Cx - Pressure Testing - Pre-Walk with GC (Podium) [Dl | 1 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7418 | Cx - Pressure Testing - GC Makes Corrections (Podiu | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7420 | Cx - Pressure Testing - Pressure Pre-Test (Podium) [D | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7422 | Cx - Pressure Testing -Corrections (Podium) [DELETE | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |

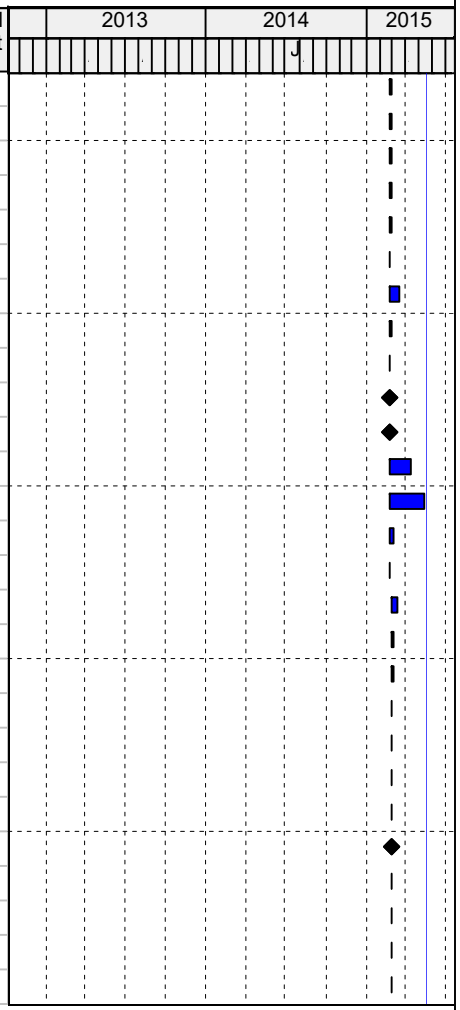


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7424 | Cx - Pressure Testing - Pressure Final Test [DELETED | 1 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7426 | Cx - Pressure Testing - Building Final Corrections [DEI | 1 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7142 | Fire Alarm System Device Testing - Podium [DELETEI | 7 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7428 | Cx - Pressure Testing - GC Indicates Tower Complete | 0 | 0 | | 01-Mar-15 A | |
| CO-7430 | Cx - Pressure Testing - Pre-Walk with GC (Tower) [DEI | 1 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7432 | Cx - Pressure Testing - GC Makes Corrections (Tower) | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7434 | Cx - Pressure Testing - Pressure Pre-Test (Tower) [DEI | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7436 | Cx - Pressure Testing -Corrections (Tower) [DELETED, | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| SW-2042 | Porte Cochere - Install trench drain | 3 | 0 | 02-Mar-15 A | 04-Mar-15 A | |
| SW-2128 | Zone 1 - FRP planter wall at NE corner | 8 | 0 | 02-Mar-15 A | 04-Mar-15 A | |
| SW-2130 | Zone 1 - Waterproof wall | 2 | 0 | 02-Mar-15 A | 02-Mar-15 A | |
| LL1-Z3-FCC36 | Install doors & hardware at FCC | 2 | 0 | 02-Mar-15 A | 02-Mar-15 A | |
| LL1-8136 | Ceramic tile in restrooms | 3 | 0 | 02-Mar-15 A | 04-Mar-15 A | |
| L1K-8218 | Floor prep | 2 | 0 | 02-Mar-15 A | 02-Mar-15 A | |
| L17-9012 | Complete Shower Surrounds | 2 | 0 | 02-Mar-15 A | 24-Apr-15 A | |
| LL2-2048 | Set Laundry Room equipment (BY OTHERS) | 1 | 0 | 03-Mar-15 A | 06-Mar-15 A | |
| L1K-8210 | Ceramic tile in restrooms | 7 | 0 | 03-Mar-15 A | 17-Mar-15 A | |
| MPT-1060 | Elevation 33/34 hat channel (east elevation, south er | 3 | 0 | 03-Mar-15 A | 10-Mar-15 A | |
| LL1-8142 | Plumbing fixtures & trim | 2 | 0 | 03-Mar-15 A | 04-Mar-15 A | |
| LL1-Z3-6038 | Paint ceiling at Food Prep (Dry Storage) | 2 | 0 | 03-Mar-15 A | 04-Mar-15 A | |
| L1B-6019 | Frame ceiling clouds | 7 | 0 | 03-Mar-15 A | 06-Mar-15 A | |
| LL1-Z3-8160 | Install doors & hardware at restrooms | 2 | 0 | 03-Mar-15 A | 04-Mar-15 A | |
| L17-9004 | Complete Flooring & Base | 3 | 0 | 03-Mar-15 A | 15-Apr-15 A | |
| CO-7116T | Fire Alarm Pre-Testing (Tower) - Tower Levels 4 thru 1( | 6 | 0 | 04-Mar-15 A | 05-Mar-15 A | |
| LL1-8150 | Install bathroom accessories | 2 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L1L-8142 | HVAC drops to 9-wood ceiling - north of Grid K | 2 | 0 | 04-Mar-15 A | 18-Mar-15 A | |
| L1L-8144 | Electrical drops to 9-wood ceiling - north of Grid K | 2 | 0 | 04-Mar-15 A | 18-Mar-15 A | |

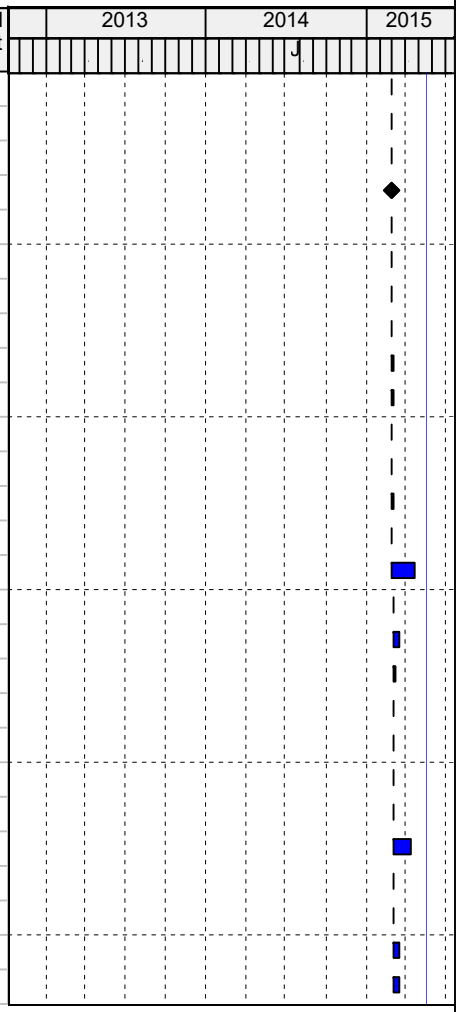


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8146 | Fire sprinkler drops to 9-wood ceiling - north of Grid K | 2 | 0 | 04-Mar-15 A | 18-Mar-15 A | |
| CO-7110T | Fire Sprinkler Pre-Testing (Tower) - Tower Levels 4 thru | 6 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| CO-7110T.1 | Fire Sprinkler Pre-Testing (Tower) - Tower Levels 3, 11 | 2 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| LL1-Z2-8150 | Install base at corridors | 3 | 0 | 05-Mar-15 A | 06-Mar-15 A | |
| L1L-8108 | GWB hang walls & ceilings (Bar) | 2 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L17-9000 | Complete GWB (1714 & 1718) | 5 | 0 | 06-Mar-15 A | 11-Mar-15 A | |
| LL1-Z2-8123 | Floor prep | 1 | 0 | 06-Mar-15 A | 06-Mar-15 A | |
| L1L-8110 | GWB tape & finish walls & ceilings (Bar) | 7 | 0 | 06-Mar-15 A | 12-Mar-15 A | |
| EL-1238 | Elev 1&2 - 30-day correction period | 30 | 0 | 07-Mar-15 A | 10-Apr-15 A | |
| L03-8624 | Fire sprinkler trim at Pool | 2 | 0 | 09-Mar-15 A | 09-Mar-15 A | |
| L11-7032 | Flooring - VCT (x42) | 1 | 0 | 09-Mar-15 A | 09-Mar-15 A | |
| SW-2212 | Zone 2 - FRP sidewalk panels | 3 | 0 | 09-Mar-15 A | 12-Mar-15 A | |
| SW-2048 | Porte Cochere - FRP Porte Cochere drive | 10 | 0 | 09-Mar-15 A | 31-Mar-15 A | |
| L03-8666 | Electrical trim & finish at ceiling at Pool | 2 | 0 | 09-Mar-15 A | 11-Mar-15 A | |
| CO-7139.1 | Install remaining devices & prep devices for testing - | 6 | 0 | 09-Mar-15 A | 12-Mar-15 A | |
| SW-2222 | Zone 2 - Install j-box at NE corner | 1 | 0 | 09-Mar-15 A | 09-Mar-15 A | |
| LL1-Z2-8146 | Floor prep at corridors | 2 | 0 | 09-Mar-15 A | 10-Mar-15 A | |
| L1L-8292 | GWB hang ceilings | 2 | 0 | 09-Mar-15 A | 10-Mar-15 A | |
| CO-7140.1 | Fire Alarm System Device Testing - Tower Levels 4 thr | 6 | 0 | 09-Mar-15 A | 12-Mar-15 A | |
| L1B-6025 | MEP drops at celing clouds (including inspection) | 7 | 0 | 09-Mar-15 A | 18-Mar-15 A | |
| L1L-8230 | Paint, prime & first coat finish | 3 | 0 | 10-Mar-15 A | 10-Mar-15 A | |
| LL2-2100 | Fire sprinkler drops to grid at Laundry | 1 | 0 | 10-Mar-15 A | 10-Mar-15 A | |
| LL1-Z2-8148 | Flooring - carpet at corridors | 3 | 0 | 10-Mar-15 A | 12-Mar-15 A | |
| L1B-8206 | Ceiling grid at West Ballrooms | 3 | 0 | 10-Mar-15 A | 11-Mar-15 A | |
| CM-1024 | Tower - "Clean/Punch" Complete - All Floors [DELETE | 0 | 0 | | 10-Mar-15 A | |
| MPT-1064 | Elevation 33/34 metal panels (east elevation, south e | 7 | 0 | 11-Mar-15 A | 26-Mar-15 A | |
| LL1-Z2-8160 | Flooring - carpet at Jr. Ballroom | 3 | 0 | 11-Mar-15 A | 13-Mar-15 A | |

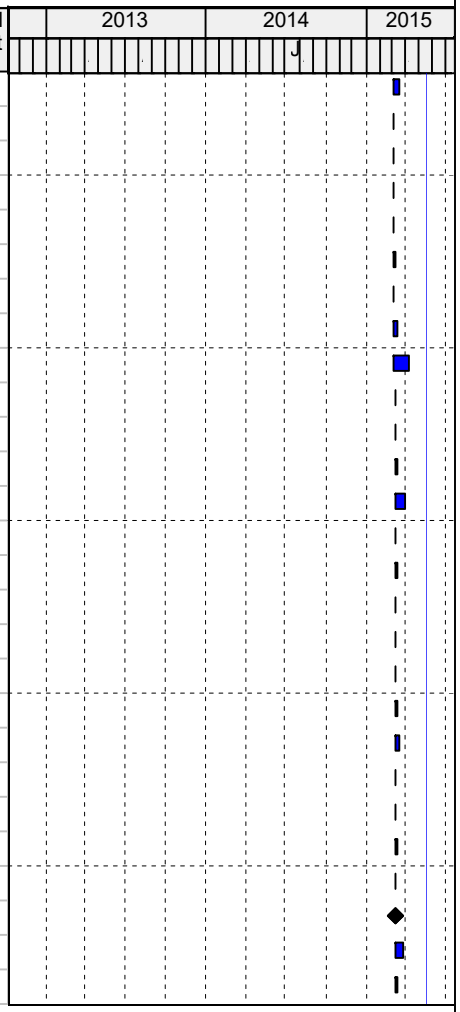



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8258 | GWB tape & finish walls & ceilings | 7 | 0 | 11-Mar-15 A | 17-Mar-15 A | |
| L1BOH2-8120 | Wall coverings - vinyl | 3 | 0 | 12-Mar-15 A | 04-May-15 A | |
| L1B-8208 | Ceiling grid at East Ballroom | 3 | 0 | 12-Mar-15 A | 13-Mar-15 A | |
| L17-9002 | Complete Painting | 2 | 0 | 12-Mar-15 A | 13-Mar-15 A | |
| L1L-8154 | Paint, prime & first finish coat (Bar) | 2 | 0 | 13-Mar-15 A | 13-Mar-15 A | |
| L1K-8206 | Install toilets at restrooms | 2 | 0 | 16-Mar-15 A | 17-Mar-15 A | |
| MPT-1082 | Caulking - Elevation 48/49 (north elevation, east of 5 | 4 | 0 | 16-Mar-15 A | 19-Mar-15 A | |
| CO-7116T.1 | Smoke Control Equipment Pre-Testing (Fans & Damp | 5 | 0 | 16-Mar-15 A | 20-Mar-15 A | |
| LL1-8128 | Floor prep at Exercise Room | 2 | 0 | 16-Mar-15 A | 16-Mar-15 A | |
| LL1-Z2-8136 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 16-Mar-15 A | 30-Mar-15 A | |
| LL4-8136 | Clear out and clean parking area | 10 | 5 | 16-Mar-15 A | 22-May-15 | 7 |
| LL3-8136 | Clear out and clean parking area | 10 | 5 | 16-Mar-15 A | 22-May-15 | 7 |
| L1L-8142a | HVAC drops to 9-wood ceiling - south of Grid K | 2 | 0 | 16-Mar-15 A | 16-Mar-15 A | |
| L1L-8144a | Electrical drops to 9-wood ceiling - south of Grid K | 2 | 0 | 16-Mar-15 A | 16-Mar-15 A | |
| L1L-8146a | Fire sprinkler drops to 9-wood ceiling - south of Grid K | 2 | 0 | 16-Mar-15 A | 16-Mar-15 A | |
| L1K-8114a | Celing grid & inspection (west end) | 2 | 0 | 16-Mar-15 A | 19-Mar-15 A | |
| CM-1016c | CM - Owner FF+E "Build-Out" - Floors 6 & 7 | 7 | 0 | 16-Mar-15 A | 22-Mar-15 A | |
| LL2-2118 | Fabricate and deliver washing machine pedestal | 10 | 0 | 16-Mar-15 A | 18-Mar-15 A | |
| I-6902 | RFI 944 - Master control panel | 5 | 0 | 16-Mar-15 A | 03-Apr-15 A | |
| LL1-8138 | Flooring - install cork floor at Exercise Room | 3 | 0 | 17-Mar-15 A | 19-Mar-15 A | |
| LL1-Z3-8206 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 17-Mar-15 A | 23-Mar-15 A | |
| L1L-8302 | Lighting & electrical trim at ceilings | 3 | 0 | 17-Mar-15 A | 18-Mar-15 A | |
| L1K-8120 | Lighting & electrical trim at ceiling | 2 | 0 | 18-Mar-15 A | 19-Mar-15 A | |
| MPP-1020 | Elevation 18/19/21/22 & complete 45 (north elevatior | 12 | 0 | 18-Mar-15 A | 27-Mar-15 A | |
| I-1208 | Paint, prime & first coat finish | 2 | 0 | 18-Mar-15 A | 19-Mar-15 A | |
| L1L-8306 | Fire sprinkler trim | 1 | 0 | 18-Mar-15 A | 18-Mar-15 A | |
| L1L-8128 | Install die wall (Bar) | 3 | 0 | 19-Mar-15 A | 23-Mar-15 A | |

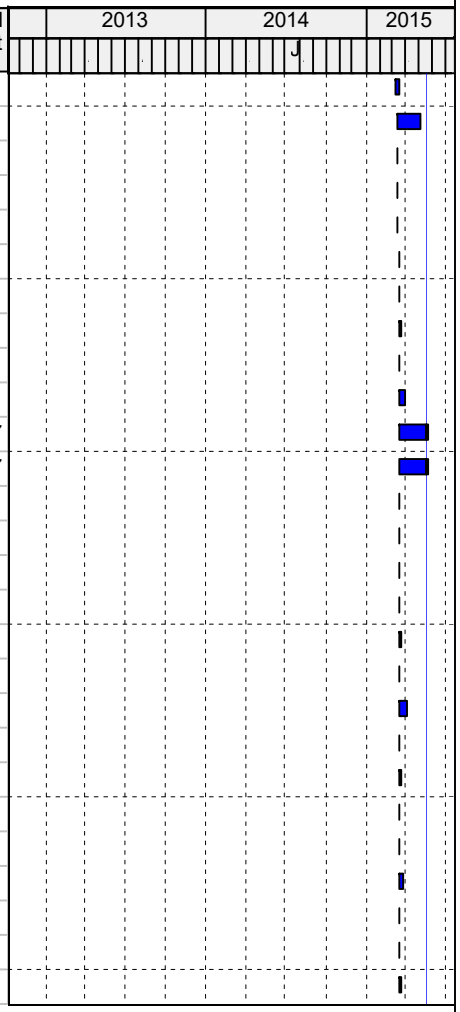



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-6037 | GWB ceiling clouds | 5 | 0 | 19-Mar-15 A | 01-Apr-15 A | |
| LL2-2114 | Install washing machine pedestal | 2 | 0 | 19-Mar-15 A | 20-Mar-15 A | |
| I-5202 | Wall and soffit modifications | 4 | 0 | 19-Mar-15 A | 03-Apr-15 A | |
| LL1-Z3-FCC34 | Paint, final coat & touch-up up at FCC | 2 | 0 | 20-Mar-15 A | 20-Mar-15 A | |
| LL2-2112 | Set washing machines | 1 | 0 | 20-Mar-15 A | 20-Mar-15 A | |
| LL1-Z3-FCC32 | Flooring - VCT at FCC | 2 | 0 | 21-Mar-15 A | 21-Mar-15 A | |
| L1BOH2-8126 | Install doors & hardware | 3 | 0 | 23-Mar-15 A | 31-Mar-15 A | |
| L1K-8128 | Install Kitchen equipment (BY OTHERS) | 5 | 0 | 23-Mar-15 A | 21-Apr-15 A | |
| L04-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L05-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L06-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L07-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L08-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L09-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L10-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L02-8130 | Ceiling grid at south half | 3 | 0 | 23-Mar-15 A | 26-Mar-15 A | |
| CO-7226 | Cx - Start-Up - Misc. Equipment | 5 | 0 | 23-Mar-15 A | 27-Mar-15 A | |
| L1BOH2C-6024 | Lighting & electrical trim at ceiling | 2 | 0 | 23-Mar-15 A | 14-Apr-15 A | |
| L1L-8136 | Install Peter Glassford art wall | 5 | 0 | 23-Mar-15 A | 27-Mar-15 A | |
| L1L-8282 | Finish carpentry/millwork | 5 | 0 | 23-Mar-15 A | 10-Apr-15 A | |
| LL1-8186a | Wall coverings - complete vinyl at corridors | 2 | 0 | 23-Mar-15 A | 24-Mar-15 A | |
| CM-1016d | CM - Owner FF+E "Build-Out" - Floors 8 & 9 | 7 | 0 | 23-Mar-15 A | 29-Mar-15 A | |
| L02-8184 | Build Kitchen exhaust shaft | 5 | 0 | 23-Mar-15 A | 27-Mar-15 A | |
| L1L-8294 | Ceiling coverings - vinyl | 3 | 0 | 23-Mar-15 A | 25-Mar-15 A | |
| L11-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L12-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L14-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |

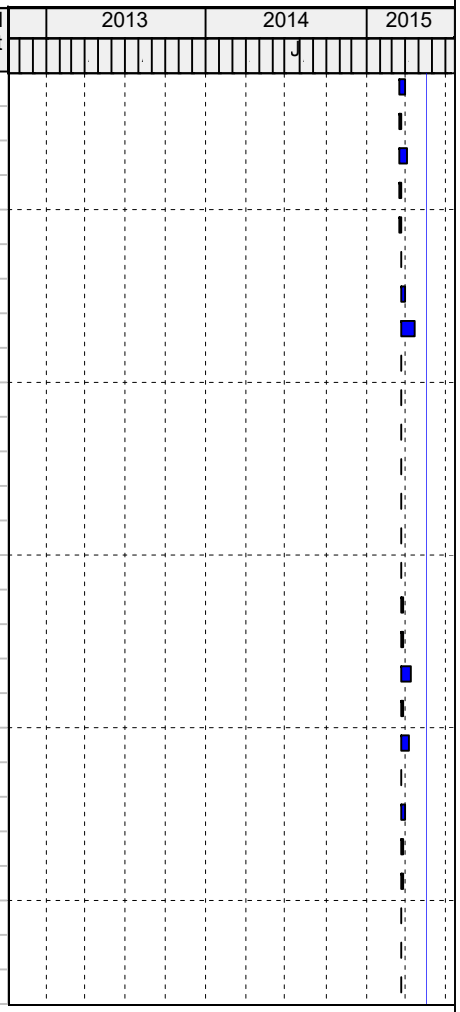



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L16-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L17-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L1K-8122 | Fire sprinkler drops/trim at ceiling | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L1K-8130 | HVAC drops/trim at celing | 2 | 0 | 24-Mar-15 A | 25-Mar-15 A | |
| L1K-8160 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 24-Mar-15 A | 25-Mar-15 A | |
| L17-9016 | Complete Shower Doors | 2 | 0 | 24-Mar-15 A | 06-May-15 A | |
| I-7010 | RFI 946 - Alterations to bar for epoxy flooring cove | 3 | 0 | 24-Mar-15 A | 30-Mar-15 A | |
| L1L-8310 | Install 9-wood ceiling supports at Sitting Area | 2 | 0 | 25-Mar-15 A | 26-Mar-15 A | |
| L1BOH2-8204 | HVAC drops/trim at ceiling | 2 | 0 | 25-Mar-15 A | 26-Mar-15 A | |
| MPT-1038 | Install louvers, north | 3 | 0 | 25-Mar-15 A | 20-Apr-15 A | |
| MPP-1048 | Caulking - Porte Cochere cornice metal | 3 | 0 | 25-Mar-15 A | 27-Mar-15 A | |
| L02-8148 | Paint at Locker Rooms | 2 | 0 | 25-Mar-15 A | 06-Apr-15 A | |
| L1K-8124a2 | Install doors & hardware | 2 | 0 | 25-Mar-15 A | 02-Apr-15 A | |
| L1L-8260 | Wall coverings - vinyl | 2 | 0 | 25-Mar-15 A | 26-Mar-15 A | |
| MPT-1106 | Install alcoves, north | 3 | 1 | 25-Mar-15 A | 20-May-15 | 2 |
| MPT-1110 | Cap metal at hi-roof | 3 | 2 | 25-Mar-15 A | 19-May-15 | 3 |
| L1L-8152 | Install ceiling (Bar) | 3 | 0 | 25-Mar-15 A | 15-Apr-15 A | |
| L1L-8116a | Finish carpentry/millwork - south of Grid K | 5 | 0 | 25-Mar-15 A | 21-Apr-15 A | |
| LL1-Z2-8142a | Wall coverings - complete vinyl at corridors | 1 | 0 | 25-Mar-15 A | 25-Mar-15 A | |
| L17-9008 | Complete Fire Sprinkler Trim | 1 | 0 | 25-Mar-15 A | 25-Mar-15 A | |
| CO-7222 | Cx - Start-Up - Kitchen Exhaust Fans | 2 | 0 | 26-Mar-15 A | 26-Mar-15 A | |
| L1K-8128a | Kitchen Equipment Final Connections | 10 | 0 | 26-Mar-15 A | 15-May-15 A | |
| CO-7260 | Cx - Start-Up - Ballroom AAON RTU | 1 | 0 | 26-Mar-15 A | 26-Mar-15 A | |
| L1L-8148 | Electrical rough-in at die wall (Bar) | 4 | 0 | 26-Mar-15 A | 31-Mar-15 A | |
| L17-9006 | Complete Lighting & Electrical Trim | 2 | 0 | 26-Mar-15 A | 31-Mar-15 A | |
| I-5084 | Zone 3 - FRP door apron at SE corner | 2 | 0 | 26-Mar-15 A | 27-Mar-15 A | |

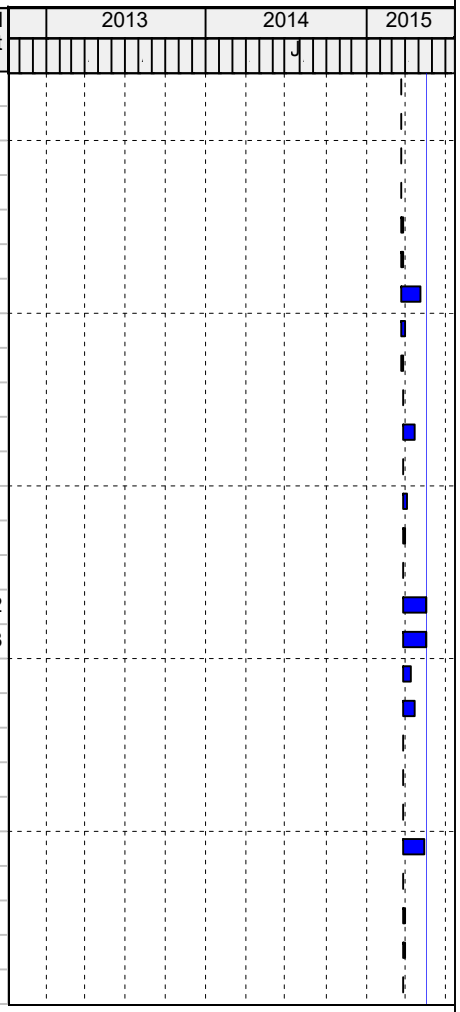



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2116 | Relocate dryers and remove floor coping at dryer area | 3 | 0 | 26-Mar-15 A | 27-Mar-15 A | |
| L1B-8176 | Complete shaft wall at Prefunction 1 south end | 4 | 0 | 26-Mar-15 A | 02-Apr-15 A | |
| L1L-8206 | Lighting & electrical trim at ceilings - north of Grid K | 2 | 0 | 26-Mar-15 A | 31-Mar-15 A | |
| LL1-Z3-8128 | Flooring - VCT | 5 | 0 | 27-Mar-15 A | 10-Apr-15 A | |
| L1L-8312 | HVAC drops to 9-wood ceiling | 2 | 0 | 27-Mar-15 A | 02-Apr-15 A | |
| L1L-8314 | Electrical drops to 9-wood ceiling | 2 | 0 | 27-Mar-15 A | 02-Apr-15 A | |
| L1L-8316 | Fire sprinkler drops to 9-wood ceiling | 2 | 0 | 27-Mar-15 A | 02-Apr-15 A | |
| L1L-8150 | Plumbing rough-in at die wall (Bar) | 4 | 0 | 27-Mar-15 A | 31-Mar-15 A | |
| CN-1000 | Install exterior canopies - steel | 5 | 0 | 27-Mar-15 A | 01-Apr-15 A | |
| L03-8682 | Install waterproofing and protection layer | 3 | 0 | 27-Mar-15 A | 02-Apr-15 A | |
| L1B-8174 | Complete grease duct insulation & inspect at Prefunc | 5 | 1 | 27-Mar-15 A | 18-May-15 | -5 |
| L17-7046 | Field mesaure and fabricate vending countertops (OF | 10 | 0 | 27-Mar-15 A | 28-Apr-15 A | |
| CO-7230 | Cx - TAB - Air Balancing - Tower | 15 | 0 | 30-Mar-15 A | 10-Apr-15 A | |
| CO-7141 | Install Fire Alarm Devices & Map to Panel - Podium | 5 | 0 | 30-Mar-15 A | 17-Apr-15 A | |
| MPT-1094 | Caulking - Elevation 32 (south elevation, east of man | 10 | 0 | 30-Mar-15 A | 10-Apr-15 A | |
| MPT-1096 | Caulking - Elevation 33/34 (east elevation, south end | 10 | 0 | 30-Mar-15 A | 10-Apr-15 A | |
| I-6012 | Core drill & install new floor drain and piping | 2 | 0 | 30-Mar-15 A | 31-Mar-15 A | |
| CM-1016b | CM - Owner FF&E "Build-Out" - Floors 10 & 11 | 7 | 0 | 30-Mar-15 A | 05-Apr-15 A | |
| LL2-2110 | Restore epoxy flooring at dryer location | 5 | 0 | 30-Mar-15 A | 03-Apr-15 A | |
| I-1204 | Finish carpentry/millwork at Concierge Lounge | 5 | 0 | 31-Mar-15 A | 07-Apr-15 A | |
| LL1-8130 | Install base | 3 | 0 | 31-Mar-15 A | 03-Apr-15 A | |
| L1L-8138 | Flooring - epoxy floor (Bar) | 5 | 0 | 31-Mar-15 A | 03-Apr-15 A | |
| L1L-8280 | Install Peter Glassford art wall | 5 | 0 | 31-Mar-15 A | 03-Apr-15 A | |
| LL1-Z2-8144 | Install doors & hardware at corridors | 2 | 0 | 31-Mar-15 A | 01-Apr-15 A | |
| L1K-8212 | Lighting & electrical trim at ceiling | 2 | 0 | 31-Mar-15 A | 01-Apr-15 A | |
| L1L-8304 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 31-Mar-15 A | 31-Mar-15 A | |
| L03-8669 | Install anchor bolts for trench drain | 1 | 0 | 31-Mar-15 A | 31-Mar-15 A | |

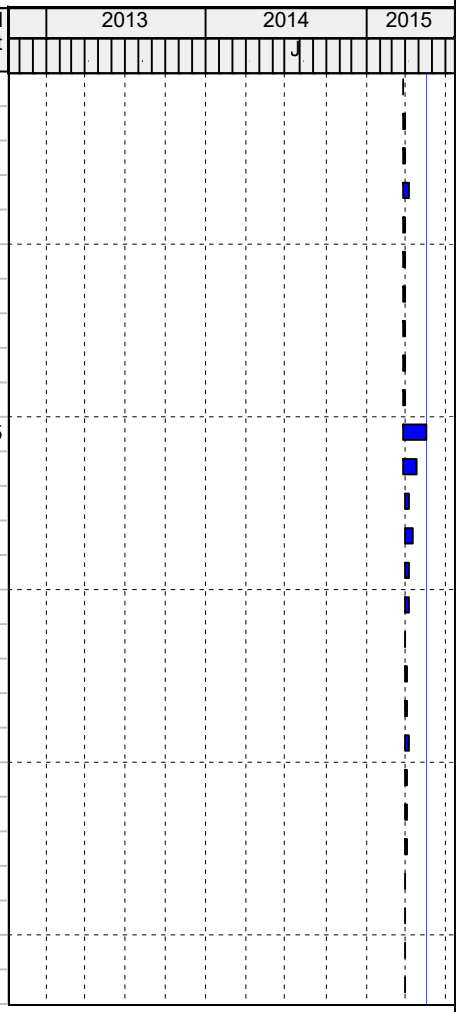


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-8178 | Complete framing & MEP at Prefunction 1 south end | 3 | 0 | 31-Mar-15 A | 02-Apr-15 A | |
| CO-7102T | Cx - DDC Point-To-Point - Central Plant [DELETED] | 5 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| L03-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7132 | Cx - DDC Point-To-Point - Ballroom VAV [DELETED] | 4 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7134 | Cx - DDC Point-To-Point - Ballroom RTU (2) [DELETEI | 2 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7402 | Cx - FPT - Central Plant [DELETED] | 2 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7406 | Cx - FPT - MUA, RTU, VAV and Exhaust Fansm [DEL | 5 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7408 | Cx - FPT - Garage Exhaust Fans [DELETED] | 1 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7410 | Cx - FPT - Misc Equipment [DELETED] | 4 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| MPT-1118 | Cap metal - Pool terrace [DELETED, INCLUDED IN G | 3 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| MPT-1120 | Cap metal at L12 Terrace [DELETED, INCLUDED IN I | 2 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| MPP-1004 | Pool Area cornice metal | 10 | 1 | 01-Apr-15 A | 20-May-15 | 2 |
| L03-8622 | HVAC trim at Pool | 2 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| LL2-2102 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 01-Apr-15 A | 06-Apr-15 A | |
| L1BOH2C-6026 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 01-Apr-15 A | 21-Apr-15 A | |
| L1L-8140a | Install 9-wood ceiling - south of Grid K | 4 | 0 | 01-Apr-15 A | 06-Apr-15 A | |
| CO-7116.1 | Smoke Control Equipment Pre-Testing (Fans & Damp | 18 | 0 | 01-Apr-15 A | 15-May-15 A | |
| L02-8158 | Ceiling grid at north half | 3 | 3 | 02-Apr-15 A | 20-May-15 | 0 |
| L03-8206a | Flooring - carpet at corridors (E-W leg) | 2 | 0 | 02-Apr-15 A | 03-Apr-15 A | |
| I-6014 | Install temporary partition at corridor | 1 | 0 | 02-Apr-15 A | 02-Apr-15 A | |
| L1L-8320 | Paint, above 9-wood ceiling | 2 | 0 | 03-Apr-15 A | 06-Apr-15 A | |
| CO-7104T.1 | Fire Alarm/Smoke Control Pre-Functional Testing - To | 10 | 0 | 06-Apr-15 A | 17-Apr-15 A | |
| L1BOH2-8116 | Finish carpentry/millwork | 5 | 0 | 06-Apr-15 A | 06-Apr-15 A | |
| LL1-Z3-FCC38 | Final clean and punch list at FCC | 3 | 0 | 06-Apr-15 A | 07-Apr-15 A | |
| MPT-1074 | Tower Sign, South (El 32) | 5 | 0 | 06-Apr-15 A | 08-Apr-15 A | |
| L1L-8130 | Install bar and back bar | 10 | 0 | 06-Apr-15 A | 21-Apr-15 A | |
| L1L-8232 | Wall coverings - vinyl | 5 | 0 | 06-Apr-15 A | 14-Apr-15 A | |

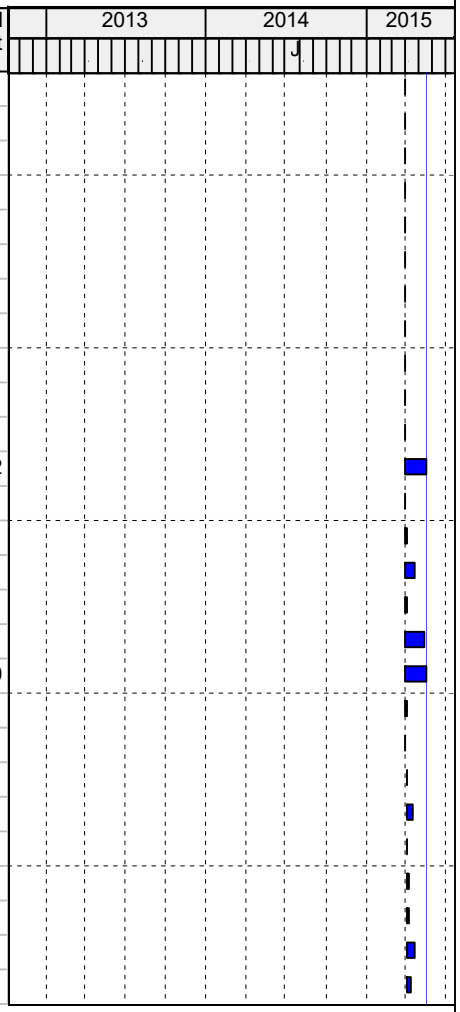



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-8142 | Paint, prime & first coat finish walls & ceilings at corrid | 2 | 0 | 06-Apr-15 A | 10-Apr-15 A | |
| L1B-8162 | Install doors & hardware at corridors | 2 | 0 | 06-Apr-15 A | 07-Apr-15 A | |
| L1L-8206a | Lighting & elecrical trim at ceilings - south of Grid K | 2 | 0 | 06-Apr-15 A | 06-Apr-15 A | |
| CM-1016e | CM - Owner FF+E "Build-Out" - Floors 12 & 14 | 7 | 0 | 06-Apr-15 A | 12-Apr-15 A | |
| SW-2050 | Street - Grind and overlay | 5 | 0 | 06-Apr-15 A | 09-Apr-15 A | |
| CN-1004 | Field measure & fabricate canopy glass | 15 | 5 | 06-Apr-15 A | 22-May-15 | 2 |
| CO-7139.2 | Install Fire Alarm Devices & Map to Panel - Tower Lev | 2 | 0 | 06-Apr-15 A | 08-Apr-15 A | |
| I-7100 | Resolve dryer duct issue | 10 | 0 | 06-Apr-15 A | 07-May-15 A | |
| I-7102 | TPAP box impact | 5 | 0 | 06-Apr-15 A | 08-May-15 A | |
| L03-8628 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L02-8140 | Lighting & electrical trim at south half | 2 | 0 | 07-Apr-15 A | 14-Apr-15 A | |
| L1L-8234 | Fire sprinkler trim at ceilings | 1 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8236 | Lighting & electrical trim at ceilings | 2 | 0 | 07-Apr-15 A | 16-Apr-15 A | |
| L1L-8262 | Fire sprinkler trim at ceilings | 1 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8264 | Lighting & electrical trim at ceilings | 3 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8266 | HVAC drops/trim at celing | 2 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8284 | Install handrails | 2 | 0 | 07-Apr-15 A | 08-Apr-15 A | |
| L1L-8298 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8318 | Install 9-wood ceiling at Sitting Area | 3 | 0 | 07-Apr-15 A | 14-Apr-15 A | |
| L1L-8204a | HVAC trim at ceiling - south of Grid K | 1 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8112a | Fire sprinkler trim - south of Grid K | 1 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| I-1206 | Install ceiling at Concierge Lounge (BOK) | 4 | 0 | 08-Apr-15 A | 09-Apr-15 A | |
| L1L-8238 | HVAC drops/trim at celing | 1 | 0 | 08-Apr-15 A | 08-Apr-15 A | |
| L1K-8128b | Ansul system final connections | 10 | 0 | 10-Apr-15 A | 15-May-15 A | |
| I-7104 | Resolve HHP issue (RFI 964) | 10 | 0 | 13-Apr-15 A | 04-May-15 A | |
| L1B-8128 | Install base at Ballrooms | 5 | 0 | 13-Apr-15 A | 17-Apr-15 A | |
| SW-2122 | Zone 1 - Install landscaping & irrigation | 15 | 0 | 13-Apr-15 A | 23-Apr-15 A | |

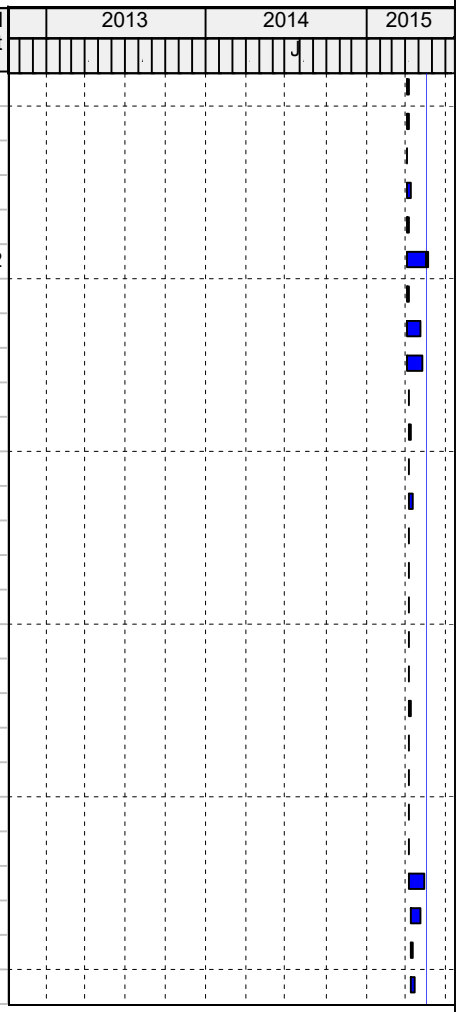



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2218 | Zone 2 - Install landscaping & irrigation | 15 | 0 | 13-Apr-15 A | 22-Apr-15 A | |
| CO-7136 | Cx - DDC Point-To-Point | 10 | 5 | 13-Apr-15 A | 22-May-15 | 8 |
| SW-2330 | Zone 3 - Landscaping & irrigation | 15 | 0 | 13-Apr-15 A | 27-Apr-15 A | |
| LL1-Z3-8158 | Install toilet partitions | 2 | 0 | 13-Apr-15 A | 14-Apr-15 A | |
| L1L-8118a | Fire alarm trim (spreaker strobe & smoke detector bas | 1 | 0 | 13-Apr-15 A | 13-Apr-15 A | |
| CM-1016f | CM - Owner FF+E "Build-Out" - Floors 15 & 16 | 7 | 0 | 13-Apr-15 A | 19-Apr-15 A | |
| CO-7231 | Cx - TAB - Air Balancing - Podium | 10 | 0 | 13-Apr-15 A | 15-May-15 A | |
| CO-7104T.3 | Compile/Certify/Accept TAB Report - Tower | 3 | 0 | 13-Apr-15 A | 15-Apr-15 A | |
| I-7200 | Owner approve pricing fo mirrors | 5 | 0 | 13-Apr-15 A | 21-Apr-15 A | |
| I-7250 | Resolve ceiling height issue at corridors | 5 | 0 | 13-Apr-15 A | 29-Apr-15 A | |
| L1BOH2-8112 | Fire sprinkler drops/trim at ceiling | 1 | 0 | 14-Apr-15 A | 14-Apr-15 A | |
| L17-8140 | Complete window sills | 1 | 0 | 14-Apr-15 A | 14-Apr-15 A | |
| L1K-8202 | Ceiling grid at Janitorial | 1 | 0 | 14-Apr-15 A | 14-Apr-15 A | |
| L1L-8242 | Finish carpentry/millwork (including front desk) | 4 | 0 | 14-Apr-15 A | 08-May-15 A | |
| L1L-8286 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 14-Apr-15 A | 14-Apr-15 A | |
| L1K-8222 | Install toilet partitions | 2 | 0 | 14-Apr-15 A | 15-Apr-15 A | |
| LL1-Z3-FCC22 | Final inspections by CoB and Fire Marshall (DELETEI | 2 | 0 | 15-Apr-15 A | 15-Apr-15 A | |
| LL1-Z3-FCC40 | Install Knox Box at FCC | 1 | 0 | 15-Apr-15 A | 15-Apr-15 A | |
| L1B-8146 | HVAC drops/trim at corridors | 2 | 0 | 15-Apr-15 A | 30-Apr-15 A | |
| L1B-8148 | Lighting & electrical trim at corridors | 2 | 0 | 15-Apr-15 A | 29-Apr-15 A | |
| L02-8156 | Install doors & hardware at north half | 3 | 0 | 15-Apr-15 A | 11-May-15 A | |
| L02-8166 | Fire sprinkler trim at north half | 2 | 2 | 15-Apr-15 A | 22-May-15 | 0 |
| SW-2068 | Street - Striping | 2 | 0 | 15-Apr-15 A | 15-Apr-15 A | |
| I-7230 | Owner provide authroization for additional backing | 2 | 0 | 15-Apr-15 A | 16-Apr-15 A | |
| L1L-8122 | Electrical trim & finish at bar (bar area final connectior | 2 | 0 | 16-Apr-15 A | 12-May-15 A | |
| L02-8114 | Floor prep at south half | 2 | 0 | 16-Apr-15 A | 17-Apr-15 A | |
| I-7210 | Owner deliver wood flooring (to Spectra's office) | 5 | 0 | 16-Apr-15 A | 28-Apr-15 A | |

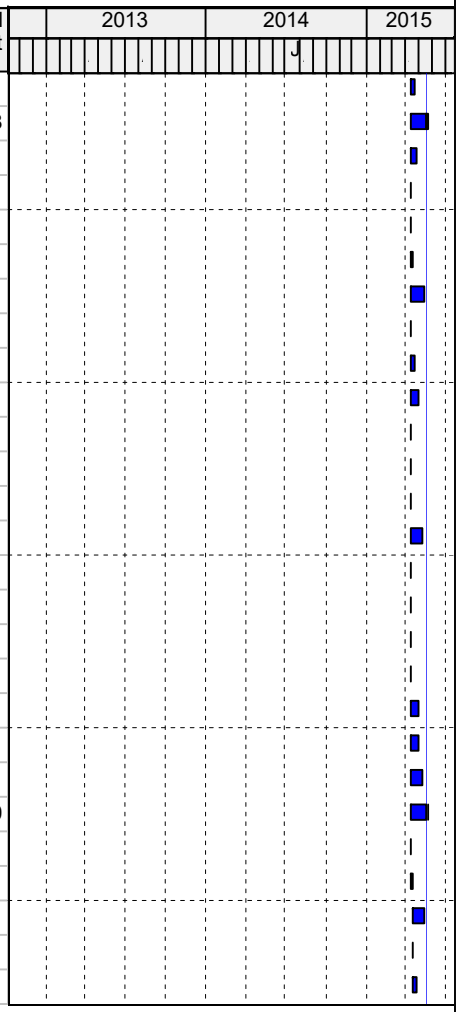



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-7222 | Fabricate and deliver bar countertops | 10 | 0 | 16-Apr-15 A | 13-May-15 A | |
| I-7224 | Owner approve change order for revised VWC installa | 3 | 0 | 16-Apr-15 A | 29-Apr-15 A | |
| L1B-8144 | Wall coverings - vinyl at corridors | 3 | 0 | 17-Apr-15 A | 11-May-15 A | |
| L02-8168 | Floor prep at north half | 1 | 0 | 17-Apr-15 A | 17-Apr-15 A | |
| LL2-8156 | Remove job shacks | 1 | 0 | 17-Apr-15 A | 24-Apr-15 A | |
| I-7220 | Owner provide direction on sink change and custom f | 10 | 0 | 17-Apr-15 A | 16-May-15 A | |
| L03-8648 | Pool Equipment Room - Install 2-hr shaft | 1 | 0 | 18-Apr-15 A | 18-Apr-15 A | |
| CM-1016a | CM - Owner FF+E "Build-Out" - Floors 3 & 17 | 7 | 0 | 20-Apr-15 A | 24-Apr-15 A | |
| LL2-8152 | Clear out and clean parking area | 10 | 5 | 20-Apr-15 A | 22-May-15 | 2 |
| L1L-8159 | Owner approve pricing for TV feature wall installation | 5 | 0 | 20-Apr-15 A | 29-Apr-15 A | |
| I-7270 | Pool Equipment Room - Re-design & layout equipme | 10 | 2 | 20-Apr-15 A | 19-May-15 | 7 |
| I-7400 | Owner approve pricing for added street signage & pro | 10 | 1 | 20-Apr-15 A | 18-May-15 | 6 |
| I-7202 | South Door - Frame Soffit | 1 | 0 | 21-Apr-15 A | 21-Apr-15 A | |
| RF-4066 | Pool Green Roof - Install decorative metal railing | 3 | 0 | 22-Apr-15 A | 23-Apr-15 A | |
| L02-8150 | Install doors & hardware at Locker Rooms | 1 | 1 | 22-Apr-15 A | 18-May-15 | 3 |
| LL2-8106b | Pinned insulation at ramp at Garage & dry shack area | 5 | 0 | 22-Apr-15 A | 28-Apr-15 A | |
| I-7204 | South Door - GWB at Soffit | 4 | 0 | 22-Apr-15 A | 29-Apr-15 A | |
| L1K-8342 | Final connections at walk-in cooler/freezer | 2 | 0 | 23-Apr-15 A | 15-May-15 A | |
| L1K-8125 | Floor prep | 1 | 0 | 23-Apr-15 A | 23-Apr-15 A | |
| L02-8152 | Flooring - VCT at south half | 10 | 0 | 23-Apr-15 A | 07-May-15 A | |
| L02-8170 | Flooring - VCT at north half | 10 | 3 | 23-Apr-15 A | 22-May-15 | 0 |
| LL1-8116a | Install countertops (owner-furnished) | 2 | 0 | 24-Apr-15 A | 30-Apr-15 A | |
| CO-7264 | Cx - Start-Up - Lobby Trane TRU (2) | 2 | 0 | 27-Apr-15 A | 28-Apr-15 A | |
| L1L-8239 | Floor prep | 2 | 0 | 27-Apr-15 A | 28-Apr-15 A | |
| L1B-8150 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 27-Apr-15 A | 28-Apr-15 A | |
| L1B-8152 | Fire sprinkler drops/trim at corridors | 1 | 0 | 27-Apr-15 A | 27-Apr-15 A | |
| LL1-8152 | Measure & fabricate mirrors | 10 | 0 | 27-Apr-15 A | 05-May-15 A | |

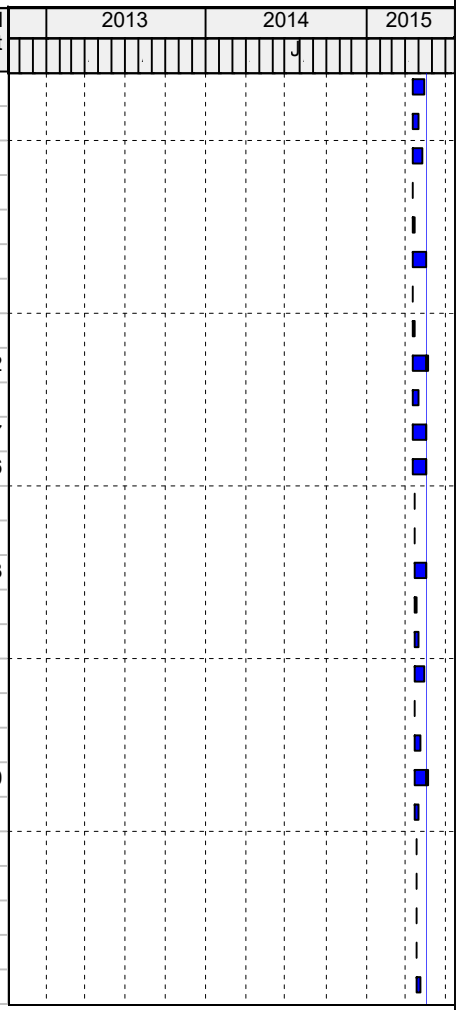



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CM-1016g | CM - Owner FF+E "Build-Out" Complete All Floors | 7 | 7 | 27-Apr-15 A | 25-May-15 | 2 |
| I-7460 | Complete ACT engineering | 5 | 0 | 27-Apr-15 A | 14-May-15 A | |
| CO-7160 | Generator - Cx generator/owner training | 3 | 0 | 28-Apr-15 A | 28-Apr-15 A | |
| L1L-8240 | Flooring - tile & base | 6 | 0 | 28-Apr-15 A | 08-May-15 A | |
| L1B-8202 | Wall coverings - vinyl at Ballrooms | 5 | 0 | 29-Apr-15 A | 07-May-15 A | |
| L02-8154 | Wall coverings - vinyl at north half | 3 | 1 | 29-Apr-15 A | 18-May-15 | 6 |
| L17-7048 | Install vending countertops (OFM) - L4-L17 | 2 | 0 | 29-Apr-15 A | 29-Apr-15 A | |
| I-7206 | South Door - Paint Soffit | 1 | 0 | 29-Apr-15 A | 29-Apr-15 A | |
| I-7212 | Deliver flooring to job site & wood flooring acclimate | 7 | 0 | 29-Apr-15 A | 07-May-15 A | |
| MPT-1084 | Caulking - Hi-roof cornice metal | 5 | 0 | 30-Apr-15 A | 01-May-15 A | |
| MPP-1018 | Elevation A/B/C (Porte Cochere wall panels) | 2 | 1 | 30-Apr-15 A | 18-May-15 | 2 |
| LL1-Z2-8116a | Install countertops (owner-furnished) | 1 | 0 | 30-Apr-15 A | 01-May-15 A | |
| I-7208 | South Door - Install wood panels | 1 | 0 | 30-Apr-15 A | 30-Apr-15 A | |
| L1L-8160 | Install TV feature wall panels/screens | 3 | 0 | 30-Apr-15 A | 07-May-15 A | |
| I-7252 | Reinstall ceiling grild at south half | 3 | 0 | 30-Apr-15 A | 07-May-15 A | |
| I-7510 | Relocate MUA 7 damper (RFI 988) | 5 | 0 | 30-Apr-15 A | 07-May-15 A | |
| SW-2232 | Zone 2 - Replace luminaire north of 3rd (DELETED) | 1 | 0 | 01-May-15 A | 01-May-15 A | |
| SW-2328 | Zone 3 - Pull wire and install light poles (DELETED) | 5 | 0 | 01-May-15 A | 01-May-15 A | |
| SW-2056 | Zone 4 - Pull wire and replace luminaires on 110th (Dl | 5 | 0 | 01-May-15 A | 01-May-15 A | |
| I-1210 | Floor prep | 2 | 0 | 01-May-15 A | 06-May-15 A | |
| I-7802 | Owner approve site lighting change order | 25 | 14 | 01-May-15 A | 05-Jun-15 | 19 |
| I-7240 | RFI 989 - Modify front desk for ADA | 10 | 0 | 01-May-15 A | 14-May-15 A | |
| MPP-1040 | Caulking - Pool Area & Ballroom cornice metal | 3 | 1 | 04-May-15 A | 22-May-15 | 5 |
| LL4-8138 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 04-May-15 A | 22-May-15 | 7 |
| LL3-8138 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 04-May-15 A | 22-May-15 | 7 |
| RF-4074 | Pool Green Roof - Install parapet coping | 6 | 0 | 04-May-15 A | 09-May-15 A | |
| I-7226 | Install revised vinyl wallcoverings | 3 | 0 | 04-May-15 A | 15-May-15 A | |

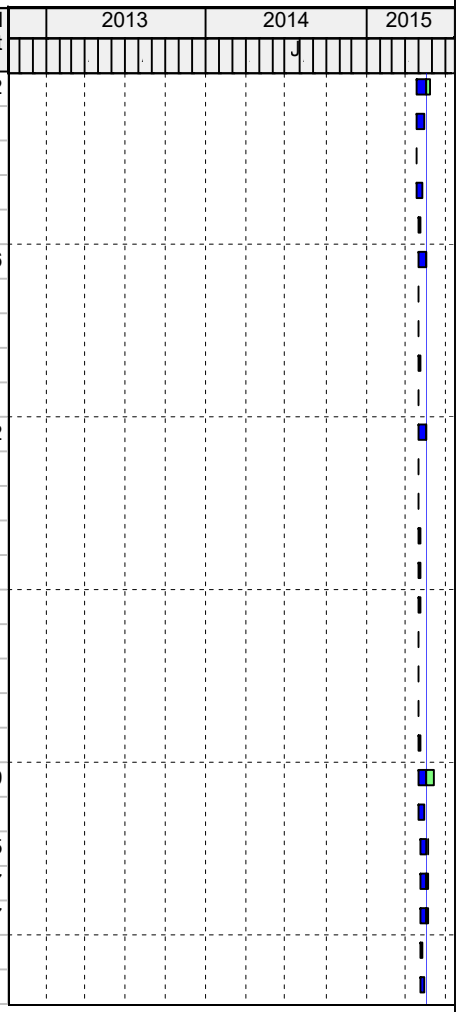



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-8198 | Paint at East Service Corridor | 3 | 0 | 04-May-15 A | 06-May-15 A | |
| I-7228 | Die wall correction notice - resolve (RFI 982) | 5 | 2 | 04-May-15 A | 19-May-15 | 1 |
| I-7236 | Owner provide remaining Kitchen equipment | 10 | 0 | 04-May-15 A | 14-May-15 A | |
| I-7108 | Restore grid ceiling | 1 | 0 | 05-May-15 A | 05-May-15 A | |
| I-7110 | Relocate lighting | 1 | 0 | 05-May-15 A | 05-May-15 A | |
| I-1202 | Flooring - tile at Concierge Lounge | 5 | 0 | 06-May-15 A | 11-May-15 A | |
| LL1-Z3-8146 | Install restroom accessories | 2 | 1 | 06-May-15 A | 21-May-15 | 3 |
| LL1-8144 | Install mirrors | 3 | 0 | 06-May-15 A | 08-May-15 A | |
| L1B-8154 | Finish carpentry/millwork at corridors | 2 | 0 | 06-May-15 A | 11-May-15 A | |
| L1B-8156 | Install base at corridors | 5 | 1 | 06-May-15 A | 26-May-15 | -2 |
| MPP-1060 | Install alcoves, south | 1 | 1 | 06-May-15 A | 21-May-15 | 6 |
| RF-4076 | Pool Green Roof - Install decorative glass | 2 | 0 | 06-May-15 A | 07-May-15 A | |
| I-7112 | Relocate sprinklers | 1 | 0 | 06-May-15 A | 06-May-15 A | |
| I-7114 | Ceiling cover inspection failure - laundry ironer - resol\ | 5 | 5 | 06-May-15 A | 22-May-15 | 0 |
| RF-4078 | TR - Terrace Roof - Install parapet coping | 6 | 0 | 07-May-15 A | 08-May-15 A | |
| L1BOH2-8201 | Paint, final coat & touch-up | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1BOH2-8118 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| LL1-8146 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| LL1-8148 | Complete acoustical ceiling tile | 2 | 2 | 07-May-15 A | 19-May-15 | 5 |
| LL1-Z3-8152 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1B-8136 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1K-8156 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1K-8158 | Complete paint final coat & touch-up | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1L-8244 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1L-8268 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| LL1-8188 | Complete paint final coat & touch-up | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| LL1-Z3-8150 | Complete paint final coat & touch-up | 2 | 0 | 07-May-15 A | 08-May-15 A | |

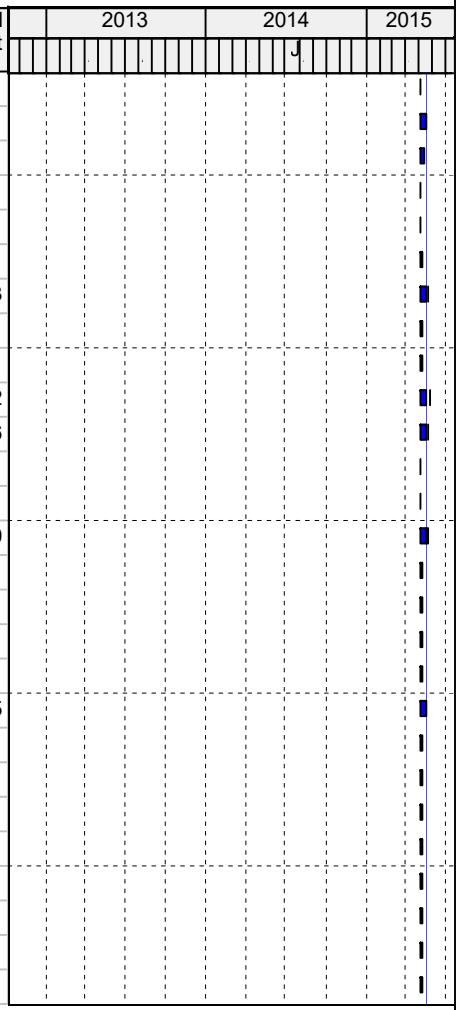



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8154 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1L-8203 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1L-8288 | Paint, final coat & touch-up | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1L-8300 | Paint, final coat & touch-up | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| MPP-1050 | Columns at Porte Cochere | 4 | 2 | 07-May-15 A | 19-May-15 | 2 |
| RF-4080 | TR - Terrace Roof - Install decorative glass | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1B-8210 | Ceiling grind at East Service Corridor | 4 | 0 | 07-May-15 A | 11-May-15 A | |
| L1L-8123 | Floor prep - north of Grid K | 2 | 0 | 08-May-15 A | 09-May-15 A | |
| LL1-Z3-8156 | Install countertops at restrooms | 2 | 1 | 08-May-15 A | 18-May-15 | 0 |
| L1L-8123a | Floor prep - south of Grid K | 2 | 0 | 08-May-15 A | 09-May-15 A | |
| I-7106 | Restore dryer wall & FRP | 5 | 1 | 08-May-15 A | 18-May-15 | 4 |
| RF-4068 | Pool Green Roof - Install American Hydrotech assemI | 3 | 0 | 11-May-15 A | 13-May-15 A | |
| RF-4070 | TR - Terrace Roof - Install American Hydrotech assem | 3 | 0 | 11-May-15 A | 13-May-15 A | |
| L02-8172 | Finish carpentry/millwork at north half | 1 | 0 | 11-May-15 A | 13-May-15 A | |
| L1L-8124b | Flooring - wood - south of Grid K | 4 | 3 | 11-May-15 A | 20-May-15 | -2 |
| I-7232 | Install additional backing (RFI 976) | 3 | 0 | 11-May-15 A | 14-May-15 A | |
| L1B-8212 | MEP drops/trim to grid at East Service Corridor (incl. i | 4 | 0 | 11-May-15 A | 13-May-15 A | |
| L1L-8123b | Floor prep - bar | 1 | 0 | 11-May-15 A | 11-May-15 A | |
| MPP-1038 | Podium Signs, West | 1 | 0 | 12-May-15 A | 12-May-15 A | |
| L1K-8220 | Install countertops in restrooms | 2 | 2 | 12-May-15 A | 20-May-15 | 0 |
| I-7810 | Replace vanity top in Women's restroom | 1 | 0 | 12-May-15 A | 15-May-15 A | |
| I-7812 | Replace vanity top in Women's restroom | 1 | 1 | 12-May-15 A | 18-May-15 | 0 |
| L1L-8120 | Plumbing fixtures & trim (Bar) | 2 | 0 | 13-May-15 A | 14-May-15 A | |
| CO-7172 | Compile/Certify/Accept TAB Report - Podium | 3 | 0 | 13-May-15 A | 15-May-15 A | |
| I-7500 | Finishes at TPA/TPB boxes | 6 | 5 | 13-May-15 A | 22-May-15 | 2 |
| LL1-Z3-8162 | Install sinks at Restrooms | 2 | 2 | 14-May-15 A | 20-May-15 | 3 |
| L03-8690 | Pool Equipment Room - Install epoxy flooring | 3 | 0 | 14-May-15 A | 16-May-15 A | |

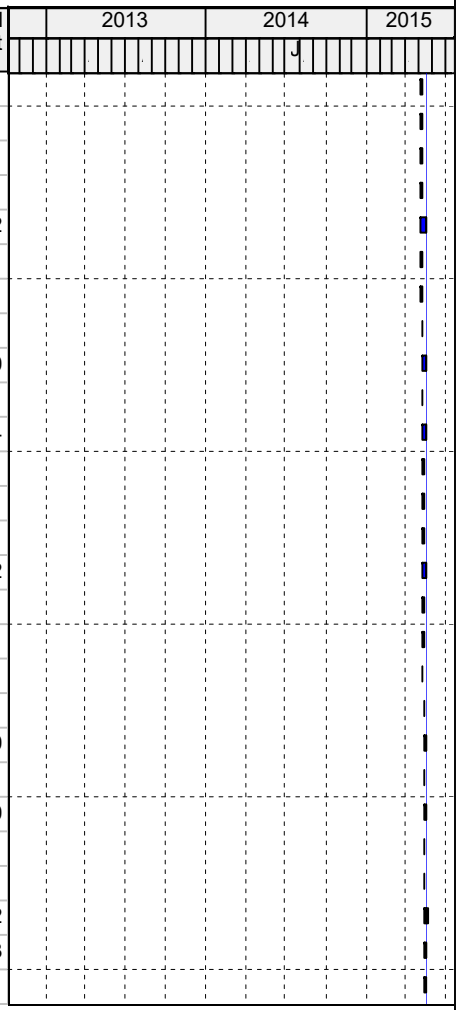



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-8216 | Floor prep at East Service Corridor | 1 | 0 | 14-May-15 A | 14-May-15 A | |
| L1B-8218 | Flooring - VCT at East Service Corridor | 2 | 0 | 14-May-15 A | 15-May-15 A | |
| I-7462 | Modify ACT grid (including inspection) | 2 | 0 | 14-May-15 A | 15-May-15 A | |
| I-7340 | Install countertops | 2 | 1 | 14-May-15 A | 18-May-15 | 4 |
| LL2-2050 | Laundry Room equipment final connections (MEP) | 3 | 2 | 15-May-15 A | 20-May-15 | 4 |
| I-1214 | Install base | 2 | 1 | 15-May-15 A | 18-May-15 | -2 |
| I-7234 | Install kitchen shelving (by owner) | 2 | 0 | 15-May-15 A | 15-May-15 A | |
| I-7238 | Install remaining Kitchen equipment | 2 | 1 | 15-May-15 A | 18-May-15 | 4 |
| I-7242 | Field measure and fabricate front desk top | 10 | 9 | 15-May-15 A | 29-May-15 | 0 |
| L1BOH2-8124 | Flooring - VCT at Luggage Room | 2 | 2 | 18-May-15 | 19-May-15 | 0 |
| L17-7032 | Flooring - VCT (x42) | 1 | 1 | 18-May-15 | 18-May-15 | 1 |
| L02-8142 | Ceiling grid at Locker Rooms | 3 | 3 | 18-May-15 | 20-May-15 | 0 |
| L1K-8154 | Complete acoustical ceiling tile | 2 | 2 | 18-May-15 | 19-May-15 | 5 |
| L1B-8129 | Floor prep | 2 | 2 | 18-May-15 | 19-May-15 | -3 |
| L1L-8308 | Floor (stair) prep | 1 | 1 | 18-May-15 | 18-May-15 | 2 |
| CO-7146 | Final Inspection - Clear & Grade | 5 | 5 | 18-May-15 | 22-May-15 | 10 |
| L1B-8196 | Install acoustical ceiling tile | 2 | 2 | 18-May-15 | 19-May-15 | -3 |
| L1BOH2-8124a | Install base | 1 | 1 | 19-May-15 | 19-May-15 | -2 |
| CO-7138 | Elevator Finals with AHJ | 6 | 6 | 19-May-15 | 27-May-15 | 8 |
| L1L-8278 | Flooring - tile at stair treads | 4 | 4 | 19-May-15 | 22-May-15 | 2 |
| L1BOH2-8123 | Floor prep | 1 | 1 | 19-May-15* | 19-May-15 | 0 |
| EL-1240 | Elev 1&2 - Final elevator inspection | 2 | 2 | 19-May-15 | 20-May-15 | 7 |
| SW-2070 | Street - Signage | 3 | 3 | 19-May-15 | 21-May-15 | 6 |
| L1L-8158 | Install bar countertops | 2 | 2 | 19-May-15 | 20-May-15 | 4 |
| L1K-8128c | City of Bellevue Kitchen approval | 2 | 2 | 19-May-15 | 20-May-15 | 4 |
| L1BOH2-8128 | Flooring - carpet | 3 | 3 | 20-May-15 | 22-May-15 | 0 |
| MPP-1056 | Caulking - Porte Cochere walls & columns | 3 | 3 | 20-May-15 | 22-May-15 | 5 |

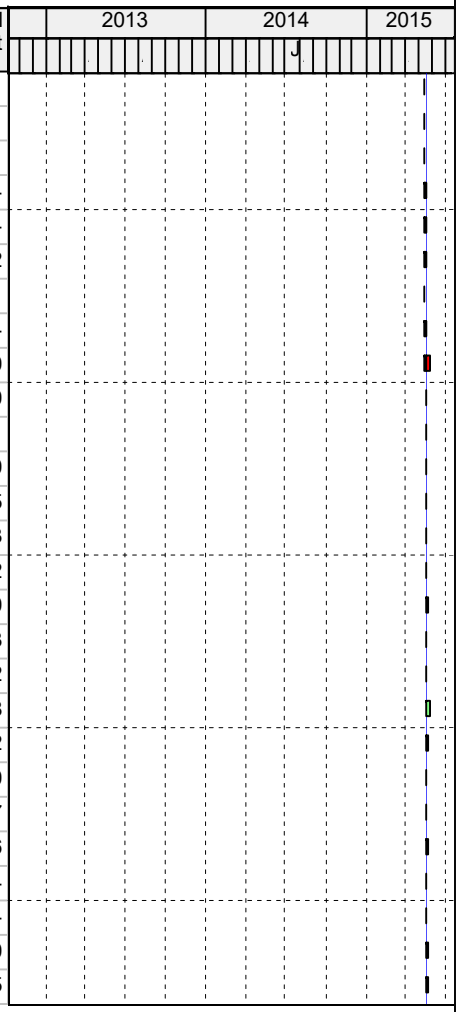



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-8190 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 20-May-15 | 27-May-15 | 5 |
| LL1-Z3-8136 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 20-May-15 | 27-May-15 | 3 |
| L03-8692 | Pool Equipment Room - Hang/tape GWB | 5 | 5 | 20-May-15 | 27-May-15 | 7 |
| L1L-8166 | Install bar front and ceramic tile | 4 | 4 | 20-May-15 | 26-May-15 | 1 |
| L1L-8322 | Install base | 2 | 2 | 20-May-15 | 21-May-15 | -2 |
| L1L-8124a | Install base | 2 | 2 | 21-May-15 | 22-May-15 | -2 |
| L03-8672 | Prep & pour pool topping slab | 2 | 2 | 21-May-15 | 22-May-15 | 0 |
| L02-8145 | MEP drops to framed ceiling (including inspections) | 2 | 2 | 21-May-15 | 22-May-15 | 0 |
| L02-8160 | HVAC drops/trim at north half | 2 | 2 | 21-May-15 | 22-May-15 | 0 |
| L02-8162 | Lighting & electrical trim at north half | 2 | 2 | 21-May-15 | 22-May-15 | 0 |
| L02-8164 | Fire alarm trim (speaker/strobe & smoke detector bas | 2 | 2 | 21-May-15 | 22-May-15 | 0 |
| MPP-1064 | Install column at Pool | 1 | 1 | 21-May-15 | 21-May-15 | 5 |
| CO-7500 | Complete Final Walsh/WPM Inspections/Corrections | 10 | 10 | 21-May-15 | 04-Jun-15 | 2 |
| L1K-8224 | Install sinks at restrooms | 2 | 2 | 21-May-15 | 22-May-15 | 0 |
| L1L-8124c | Flooring - tile - in front of bar | 4 | 4 | 21-May-15 | 27-May-15 | 0 |
| L1L-8162 | Install quartz base at TV feature wall | 3 | 3 | 21-May-15 | 26-May-15 | -1 |
| I-7116 | Finishes at TPA/TPB boxes | 2 | 2 | 21-May-15 | 22-May-15 | 2 |
| CM-1018.1 | CM - Kitchen Burn-In & Training | 14 | 14 | 21-May-15 | 03-Jun-15 | 7 |
| CO-7144 | Final Inspection - Transportation (Right-Of-Way) | 5 | 5 | 22-May-15 | 29-May-15 | 6 |
| CO-7148 | Final Inspection - Utilities | 5 | 5 | 22-May-15 | 29-May-15 | 6 |
| L1L-8296 | Install walk-off mat | 1 | 1 | 22-May-15 | 22-May-15 | 2 |
| I-1216 | Flooring - install carpet insert | 1 | 1 | 22-May-15 | 22-May-15 | 2 |
| L1BOH2-8140 | Acoustical ceiling tile | 2 | 2 | 26-May-15 | 27-May-15 | 0 |
| L02-8138 | Complete acoustical ceiling tile | 2 | 2 | 26-May-15 | 27-May-15 | 0 |
| L1K-8208 | Install restroom accessories | 2 | 2 | 26-May-15 | 27-May-15 | 0 |
| L03-8670 | Installl trench drains at Pool | 2 | 2 | 26-May-15 | 27-May-15 | 0 |
| LL2-8144 | Complete acoustical ceiling tile | 2 | 2 | 26-May-15 | 27-May-15 | 0 |

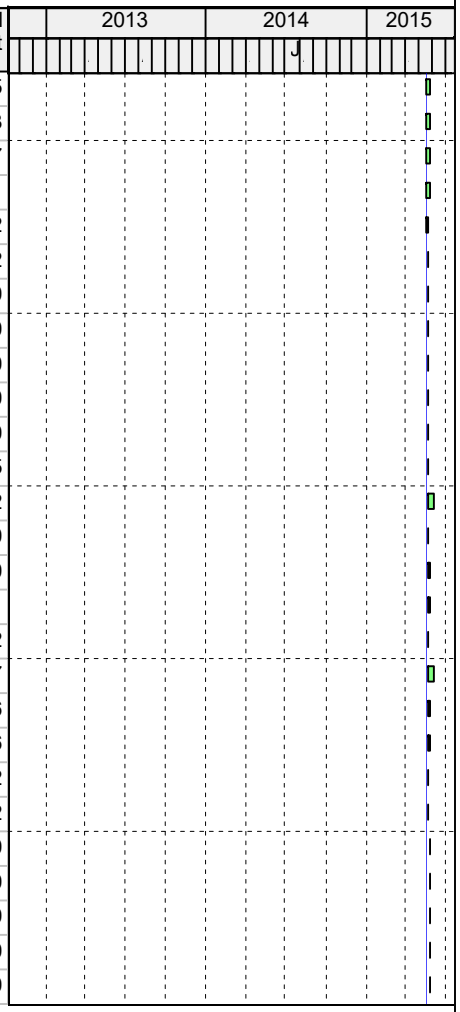



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-8160 | Floor prep | 2 | 2 | 26-May-15 | 27-May-15 | -3 |
| CN-1002 | Install exterior canopies - glass | 3 | 3 | 26-May-15 | 28-May-15 | 2 |
| LL1-Z2-8162 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 26-May-15 | 01-Jun-15 | 2 |
| L1L-8164 | Complete TV feature wall panels/screens | 2 | 2 | 27-May-15 | 28-May-15 | -1 |
| L1B-8130 | Flooring - VCT at A/V room | 2 | 2 | 28-May-15 | 29-May-15 | -2 |
| L1B-8158 | Flooring - carpet at south corridor & Prefunction 1 | 3 | 3 | 28-May-15 | 01-Jun-15 | -3 |
| CO-7156 | Final Inspection - Health Department (Kitchens) | 5 | 5 | 28-May-15 | 03-Jun-15 | 3 |
| LL2-8154 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 28-May-15 | 03-Jun-15 | 0 |
| L1BOH2-8136 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 28-May-15 | 03-Jun-15 | 0 |
| L1K-8166 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 28-May-15 | 03-Jun-15 | 0 |
| L02-8182 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 28-May-15 | 03-Jun-15 | 0 |
| L03-8688 | Complete pool topping slab | 2 | 2 | 28-May-15 | 29-May-15 | 0 |
| L1B-8168 | Wall coverings - vinyl at Prefunction 2 | 2 | 2 | 28-May-15 | 29-May-15 | -4 |
| L1B-8180 | HVAC drops/trim at Prefunction 2 | 2 | 2 | 28-May-15 | 29-May-15 | -3 |
| L1B-8182 | Lighting & electrical trim at Prefunction 2 | 2 | 2 | 28-May-15 | 29-May-15 | -3 |
| L1B-8184 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 2 | 28-May-15 | 29-May-15 | -3 |
| L1B-8166 | Install operable partition doors | 2 | 2 | 28-May-15 | 29-May-15 | -2 |
| L03-8694 | Pool Equipment Room - Paint | 2 | 2 | 28-May-15 | 29-May-15 | 7 |
| CO-7150 | Final Inspection - Electrical | 5 | 5 | 29-May-15 | 04-Jun-15 | 2 |
| L1L-8156 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 29-May-15 | 04-Jun-15 | -1 |
| L03-8674 | Install storefront at Pool entry | 2 | 2 | 01-Jun-15 | 02-Jun-15 | 6 |
| CO-7152 | Final Inspection - Plumbing | 5 | 5 | 01-Jun-15 | 05-Jun-15 | 1 |
| CO-7154 | Final Inspection - Mechanical | 5 | 5 | 01-Jun-15 | 05-Jun-15 | 1 |
| L1B-8186 | Fire sprinkler drops/trim at Prefunction 2 | 1 | 1 | 01-Jun-15 | 01-Jun-15 | -3 |
| L1B-8188 | Finish carpentry/millwork at Prefunction 2 | 2 | 2 | 01-Jun-15 | 02-Jun-15 | -4 |
| L1B-8190 | Install base at Prefunction 2 | 2 | 2 | 01-Jun-15 | 02-Jun-15 | -4 |
| L1B-8194 | Floor prep at Prefunction 2 | 1 | 1 | 01-Jun-15 | 01-Jun-15 | -3 |

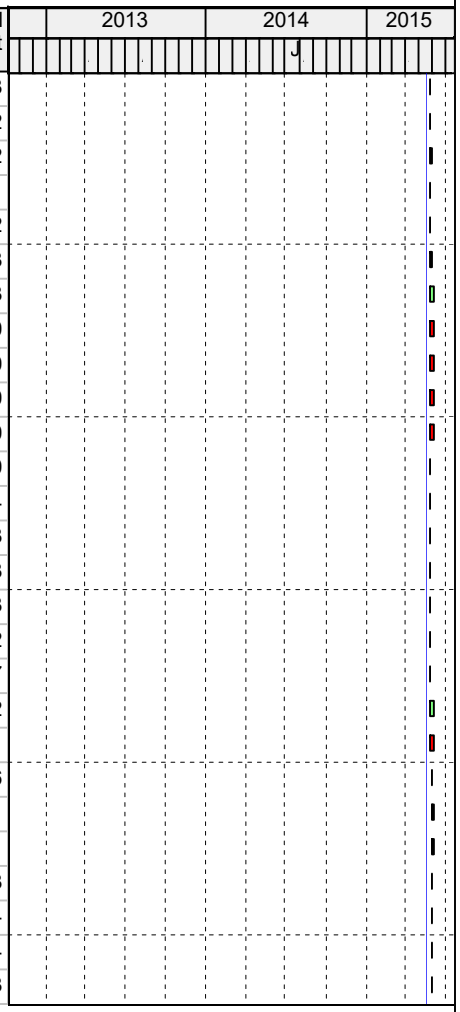



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8696 | Pool Equipment Room - Install pool equipment | 3 | 3 | 01-Jun-15 | 03-Jun-15 | 7 |
| I-7244 | Install front desk top | 1 | 1 | 01-Jun-15 | 01-Jun-15 | 0 |
| I-7246 | Complete connections at front desk | 1 | 1 | 02-Jun-15 | 02-Jun-15 | 0 |
| L1B-8172 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 03-Jun-15 | 09-Jun-15 | -4 |
| L1B-8192 | Flooring - carpet at Prefunction 2 | 2 | 2 | 03-Jun-15 | 04-Jun-15 | -4 |
| L1BOH2-8134 | Final Cleaning | 2 | 2 | 04-Jun-15 | 05-Jun-15 | 0 |
| L1BOH2-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 08-Jun-15 | 10-Jun-15 | 0 |
| CO-7124 | Final Inspection - Building Department | 2 | 2 | 08-Jun-15 | 09-Jun-15 | 1 |
| L03-8640 | Prep and install pool plaster | 3 | 3 | 08-Jun-15 | 10-Jun-15 | 0 |
| SW-2228 | Install street lighting - All site zones | 5 | 5 | 08-Jun-15 | 12-Jun-15 | 19 |
| L1BOH2-81214 | L1, Zone 3 Complete | 0 | 0 | | 10-Jun-15 | 0 |
| LL2-8150 | LL2 Floor Complete | 0 | 0 | | 10-Jun-15 | 0 |
| L03-8618 | Ceramic tile at pool area | 8 | 8 | 11-Jun-15 | 22-Jun-15 | 0 |
| L03-8642 | Fill pool | 1 | 1 | 11-Jun-15 | 11-Jun-15 | 1 |
| L03-8644 | Connect, startup & adjust pool equipment | 10 | 10 | 12-Jun-15 | 25-Jun-15 | 1 |
| I-7000 | Owner post bond for site lighting for TCO (if necessar | 0 | 0 | | 12-Jun-15 | 22 |
| CO-7170 | Final inspections - Site Lighting | 2 | 2 | 15-Jun-15 | 16-Jun-15 | 19 |
| CM-1022 | Podium - "Clean/Punch" Complete - All Floors, All Zon | 0 | 0 | | 16-Jun-15 | -4 |
| L03-8620 | Plumbing fixtures & trim at Pool | 2 | 2 | 23-Jun-15 | 24-Jun-15 | 0 |
| L03-8626 | Electrical trim & finish at Pool | 2 | 2 | 23-Jun-15 | 24-Jun-15 | 0 |
| L03-8630 | Install doors & hardware at Pool | 2 | 2 | 23-Jun-15 | 24-Jun-15 | 2 |
| L03-8638 | Install pool deck and ADA lift | 3 | 3 | 23-Jun-15 | 25-Jun-15 | 1 |
| L03-8632 | Install restroom accessories at Pool | 2 | 2 | 25-Jun-15 | 26-Jun-15 | 0 |
| L03-8646 | Health inspection | 1 | 1 | 29-Jun-15 | 29-Jun-15 | 0 |
| L03-8676 | Contractor Punchlist at Pool (inspect/distribute/correct | 3 | 3 | 30-Jun-15 | 02-Jul-15 | 0 |
| L03-8680 | Final Cleaning at Pool | 2 | 2 | 06-Jul-15 | 07-Jul-15 | 0 |
| L03-8678 | Owner Punchlist at Pool (inspect/distribute/correct) | 3 | 3 | 08-Jul-15 | 10-Jul-15 | 0 |

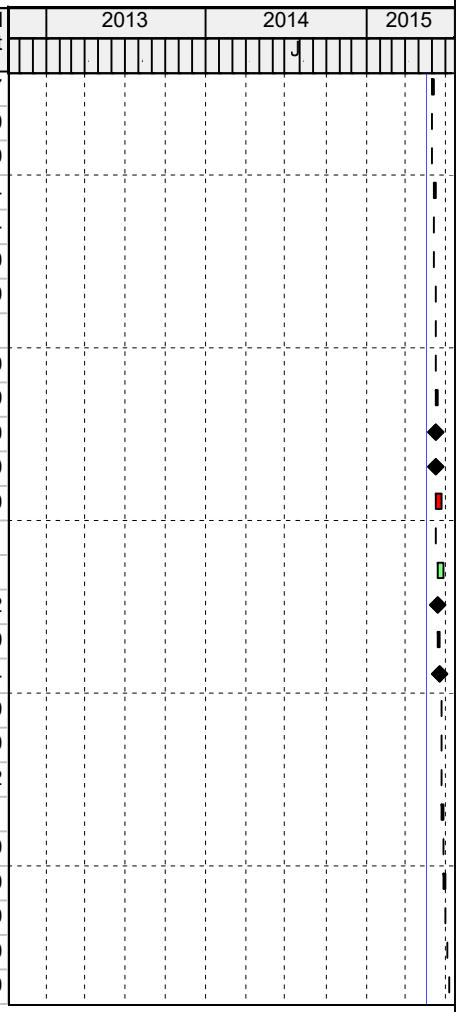



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7168 | Final Inspections - Pool | 2 | 2 | 13-Jul-15 | 14-Jul-15 | 0 |
| CO-7008 | Substantial Completion - Pool & Site Lighting | 0 | 0 | | 14-Jul-15 | 0 |
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13 A | | |
| CM-1002 | CM - Contract Time (578 Cal Days) | 576 | 0 | 06-Mar-13 A | 05-Oct-14 A | |
| CM-1014 | CM - Start of Construction | 0 | 0 | 05-Apr-13 A | | |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 09-Mar-15 A | | |
| CM-1016 | CM - Owner FF+E "Build-Out" - Floors 4 & 5 | 7 | 0 | 09-Mar-15 A | 15-Mar-15 A | |
| CM-1006 | Construction Documents Issued by Client - (Due on 7 | 0 | 0 | 18-May-15 | | 24 |
| CM-1008 | Finalization of Allowances - (Due on 9-2-13) | 0 | 0 | 18-May-15 | | 24 |
| CM-1018 | CM - Hotel Operations Training | 14 | 14 | 26-May-15 | 08-Jun-15 | 2 |
| CO-7004 | CO - Prep / Submit O&M Manuals | 14 | 14 | 26-May-15 | 08-Jun-15 | 2 |
| CO-7122 | TCO - Temporary Certificate of Occupancy | 0 | 0 | | 09-Jun-15 | 1 |
| CO-7006 | TCO - Temporary Certificate of Occupancy/Substantia | 0 | 0 | | 16-Jun-15* | -6 |
| **Misc Milestones** | | | | | | |
| CM-1020 | MM - Site Mobilization | 10 | 0 | 06-Mar-13 A | 04-Apr-13 A | |
| MM-1008 | MM - Top Out - Tower / Structure | 0 | 0 | | 16-Apr-14 A | |
| MM-1004 | MM - Start Drywall In Tower | 0 | 0 | 27-Jun-14 A | | |
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 06-Sep-14 A | |
| MM-1010 | Energize Permanent Power | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| **Tower Crane** | | | | | | |
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 0 | 04-Jun-13 A | 14-Jun-13 A | |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 0 | 20-Jun-13 A | 24-Jun-13 A | |

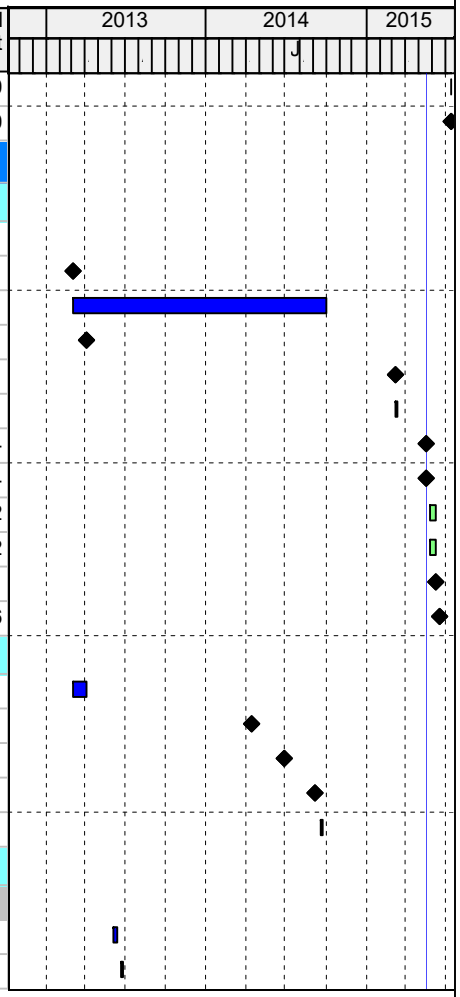


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| TC-5902 | Tower Crane - Erectiion | 2 | 0 | 21-Jun-13 A | 24-Jun-13 A | |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 24-Jun-13 A | | |
| TC-5906 | Tower Crane - Operatational Period | 391 | 0 | 24-Jun-13 A | 16-Jun-14 A | |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 0 | 16-Jun-14 A | 17-Jun-14 A | |
| **Man & Material Lifts** | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 0 | 14-Jan-14 A | 20-Jan-14 A | |
| ML-5952 | Man/Material Lifts - Erect/Build Loading Dock | 5 | 0 | 21-Jan-14 A | 27-Jan-14 A | |
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 10-Feb-14 A | | |
| ML-5954 | Man/Material Lifts - Load Test / Certify | 1 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| ML-5958 | Man/Material Lifts - Operatational Period | 196 | 0 | 10-Feb-14 A | 15-Nov-14 A | |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 2 | 0 | 15-Nov-14 A | 16-Nov-14 A | |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |
| **Mass Excavation / Shoring** | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 0 | 05-Apr-13 A | 12-Apr-13 A | |
| SW-2002 | Demolition And Utility Relocation | 8 | 0 | 15-Apr-13 A | 19-Apr-13 A | |
| SW-2010 | Grade Subgrade for Elect/Plumbing | 3 | 0 | 07-Jan-14 A | 09-Jan-14 A | |
| **Site Finishes** | | | | | | |
| SW-2006 | Install Perm Power Electrical Service / Dry Utilities (Ofl | 15 | 0 | 20-May-14 A | 05-Jun-14 A | |
| SW-2004 | Offsite Water & Water Connection | 9 | 0 | 22-Sep-14 A | 01-Oct-14 A | |
| SW-2008 | Zone 4 - Landscaping & irrigation | 15 | 0 | 13-Apr-15 A | 27-Apr-15 A | |
| **Structure** | | | | | | |
| **Foundation / Substructure - (Levels LL4 / LL3)** | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 0 | 12-Jun-13 A | 27-Jun-13 A | |
| LL4-1601 | LL4 - Excavate Footings | 14 | 0 | 17-Jun-13 A | 30-Jul-13 A | |

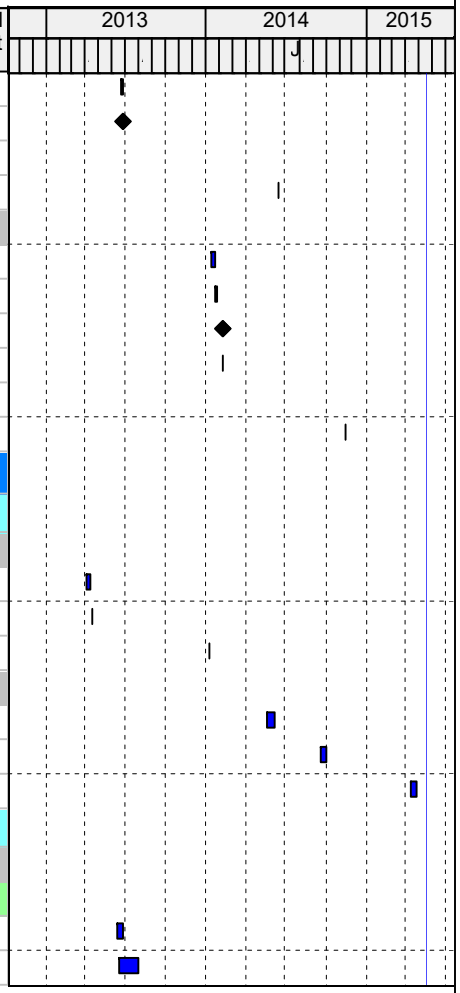


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 0 | 18-Jun-13 A | 24-Jun-13 A | |
| LL4-1606 | LL4 - Undrgrnd Plumbing | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-1608 | LL4 - Undrgrnd Elec | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 0 | 19-Jun-13 A | 25-Jun-13 A | |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 0 | 26-Jun-13 A | 02-Aug-13 A | |
| LL4-2033 | LL4 - Shotcrete Walls | 27 | 0 | 26-Jun-13 A | 05-Aug-13 A | |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 0 | 03-Jul-13 A | 21-Aug-13 A | |
| LL4-1614 | LL4 - FRP SOG | 5 | 0 | 10-Jul-13 A | 07-Aug-13 A | |
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 0 | 12-Jul-13 A | 26-Jul-13 A | |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 0 | 13-Jul-13 A | 06-Aug-13 A | |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 0 | 22-Jul-13 A | 24-Jul-13 A | |
| LL4-1618 | LL4 - FRP Ramp SOG | 5 | 0 | 01-Aug-13 A | 07-Aug-13 A | |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2004 | LL2 - Shore / Form Deck | 8 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2006 | LL3 - M & E Inserts | 4 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2008 | LL3 - ReSteel / PT Cables | 6 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2010 | LL3 - Install Embeds | 2 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2001 | LL3 - Waterproof Walls | 3 | 0 | 05-Aug-13 A | 05-Aug-13 A | |
| LL3-2012 | LL3 - Pour / Finish Deck | 2 | 0 | 16-Aug-13 A | 16-Aug-13 A | |
| LL3-2014 | LL3 - Stress Tendons | 1 | 0 | 19-Aug-13 A | 19-Aug-13 A | |
| LL3-2000 | LL3 - FRP Core Walls | 8 | 0 | 19-Aug-13 A | 28-Aug-13 A | |
| LL3-2033 | LL3 - Shotcrete Walls | 5 | 0 | 23-Aug-13 A | 26-Aug-13 A | |
| LL3-2016 | LL3 - Strip / ReShore Deck | 3 | 0 | 01-Sep-13 A | 13-Sep-13 A | |
| LL3-2018 | LL3 - Remove ReShores | 4 | 0 | 04-Nov-13 A | 07-Nov-13 A | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Grids 1 to 4 - (SOG @ Loading Dock)** | | | | | | |

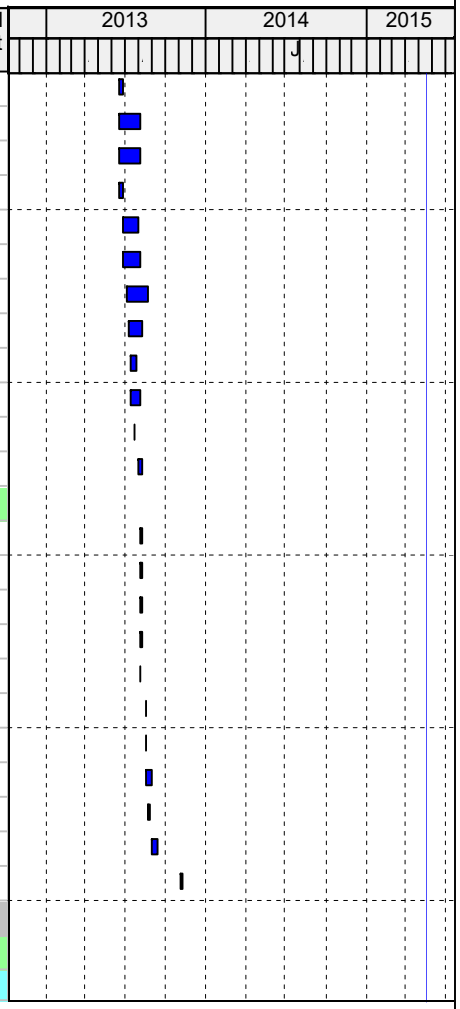



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2056 | LL2 - Grease Intercepter | 5 | 0 | 15-Aug-13 A | 21-Aug-13 A | |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 0 | 27-Aug-13 A | 04-Sep-13 A | |
| LL2-2027 | LL2 - Waterproof Walls | 2 | 0 | 27-Aug-13 A | 28-Aug-13 A | |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 0 | 30-Aug-13 A | 05-Sep-13 A | |
| LL2-2021 | LL2 - FRP Elec Vault | 14 | 0 | 30-Aug-13 A | 04-Sep-13 A | |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 0 | 04-Sep-13 A | 11-Sep-13 A | |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 0 | 11-Sep-13 A | 13-Sep-13 A | |
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls/Roof | 11 | 0 | 19-Sep-13 A | 03-Oct-13 A | |
| LL2-2020 | LL2 - Undrgmd Plumbing | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2022 | LL2 - Undrgmd Elec | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2031 | LL2 - FRP Generator SOG | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2015 | LL2 to LL1 FRP Columns / Misc Walls | 6 | 0 | 01-Oct-13 A | 01-Oct-13 A | |
| LL2-2029 | LL2 - F/R/P Pour #2 | 8 | 0 | 15-Jan-14 A | 24-Jan-14 A | |
| LL2-2011 | LL2 - F/R/P Pour #3 | 16 | 0 | 24-Jan-14 A | 18-Feb-14 A | |
| LL2-2019 | LL2 - F/R/P Pour #6 | 4 | 0 | 19-Feb-14 A | 17-Mar-14 A | |
| LL2-2044 | LL2 - Set Generator | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |
| LL2-2004 | LL2 - Shore / Form Deck | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2035 | LL2 to LL1 - Shotcrete Walls | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2006 | LL2 - M & E Inserts | 4 | 0 | 14-Aug-13 A | 19-Aug-13 A | |
| LL2-2008 | LL2 - ReSteel / PT Cables | 6 | 0 | 14-Aug-13 A | 21-Aug-13 A | |
| LL2-2010 | LL2 - Install Embeds | 3 | 0 | 14-Aug-13 A | 16-Aug-13 A | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 0 | 27-Aug-13 A | 06-Sep-13 A | |
| LL2-2012 | LL2 - Place / Finish Deck | 3 | 0 | 29-Aug-13 A | 29-Aug-13 A | |
| LL2-2023 | LL2 - Waterproof Walls | 3 | 0 | 29-Aug-13 A | 03-Sep-13 A | |
| LL2-2014 | LL2 - Stress Tendons | 1 | 0 | 30-Aug-13 A | 30-Aug-13 A | |

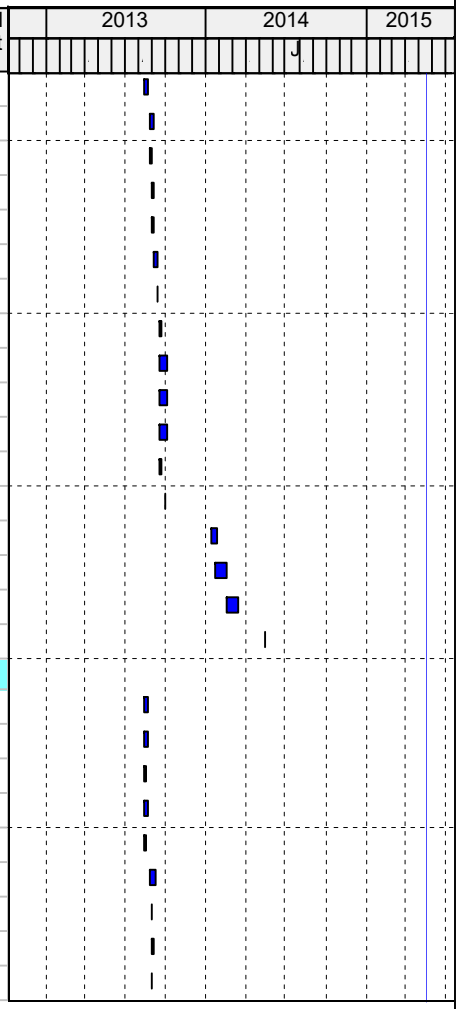



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2016 | LL2 - Strip / ReShore | 3 | 0 | 03-Sep-13 A | 05-Sep-13 A | |
| LL2-8234 | LL2 - Place / Finish Deck | 3 | 0 | 12-Sep-13 A | 12-Sep-13 A | |
| LL2-2000 | LL2 - FRP Core Walls | 8 | 0 | 12-Sep-13 A | 23-Sep-13 A | |
| LL2-2018 | LL2 - Remove ReShores | 4 | 0 | 13-Nov-13 A | 18-Nov-13 A | |
| LL2-2013 | LL2 - F/R/P Pour #1 | 4 | 0 | 13-Jan-14 A | 16-Jan-14 A | |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| P5A-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2000 | LL1 - FRP Core Walls | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2004 | LL1 - Shore / Form Deck | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| P6-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P6-2004 | LL1 - Shore / Form Deck | 7 | 0 | 16-Sep-13 A | 24-Sep-13 A | |
| P5A-2006 | LL1 - MEP Rough In | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2008 | LL1 - ReSteel / PT Cables | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2012 | LL1 - Place / Finish Deck | 0 | 0 | 20-Sep-13 A | | |
| P5A-2020 | LL1 - Waterproof Walls | 3 | 0 | 20-Sep-13 A | 24-Sep-13 A | |
| P5A-2014 | LL1 - Stress Tendons | 1 | 0 | 23-Sep-13 A | 23-Sep-13 A | |
| P5A-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2006 | LL1 - MEP Rough In | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2008 | LL1 - ReSteel / PT Cables | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 24-Sep-13 A | 25-Sep-13 A | |
| P6-2020 | LL1 - Waterproof Walls | 4 | 0 | 24-Sep-13 A | 27-Sep-13 A | |
| P5A-2033 | LL1 - Resteel/Shotcrete Walls | 3 | 0 | 25-Sep-13 A | 27-Sep-13 A | |
| P5B-2002 | LL1 - FRP Columns Below | 5 | 0 | 26-Sep-13 A | 02-Oct-13 A | |
| P5B-2004 | LL1 - Shore / Form Deck | 7 | 0 | 26-Sep-13 A | 04-Oct-13 A | |
| P6-2012 | LL1 - Place / Finish Deck | 0 | 0 | 27-Sep-13 A | | |
| P6-2014 | LL1 - Stress Tendons | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |

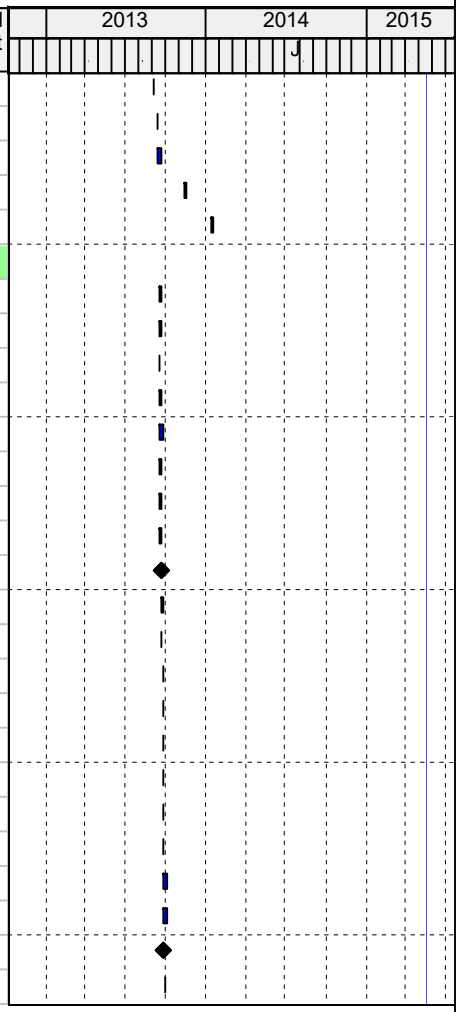



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P6-2033 | LL1 - Resteel/Shotcrete Walls | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 01-Oct-13 A | 03-Oct-13 A | |
| P5B-2006 | LL1 - MEP Rough In | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2002 | FRP Columns Below | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2004 | Shore / Form Deck | 4 | 0 | 03-Oct-13 A | 08-Oct-13 A | |
| P5B-2008 | LL1 - ReSteel / PT Cables | 5 | 0 | 04-Oct-13 A | 10-Oct-13 A | |
| P5B-2010 | LL1 - Install Edgeform/Embeds | 4 | 0 | 04-Oct-13 A | 09-Oct-13 A | |
| P8-2002 | FRP Columns Below | 5 | 0 | 07-Oct-13 A | 11-Oct-13 A | |
| P8-2000 | Form/Resteel/Close Core Walls | 14 | 0 | 07-Oct-13 A | 24-Oct-13 A | |
| P8-2004 | Shore / Form Deck P8 | 8 | 0 | 07-Oct-13 A | 16-Oct-13 A | |
| P7-2002 | FRP Columns Below | 5 | 0 | 08-Oct-13 A | 14-Oct-13 A | |
| P7-2004 | Shore / Form Deck | 6 | 0 | 08-Oct-13 A | 15-Oct-13 A | |
| P10A--2006 | MEP Rough In | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2008 | ReSteel / PT Cables | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2010 | Install Edgeform/Embeds | 2 | 0 | 08-Oct-13 A | 09-Oct-13 A | |
| P5B-2012 | LL1 - Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P10A--2012 | Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P5B-2014 | LL1 - Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P7-2006 | MEP Rough In | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P7-2008 | ReSteel / PT Cables | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P10A--2014 | Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P8-2020 | Shore / Form Deck P9 | 6 | 0 | 14-Oct-13 A | 21-Oct-13 A | |
| P5B-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2010 | Install Edgeform/Embeds | 2 | 0 | 15-Oct-13 A | 16-Oct-13 A | |
| P8-2006 | MEP Rough In | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2008 | ReSteel / PT Cables | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2010 | Install Edgeform/Embeds | 4 | 0 | 15-Oct-13 A | 18-Oct-13 A | |

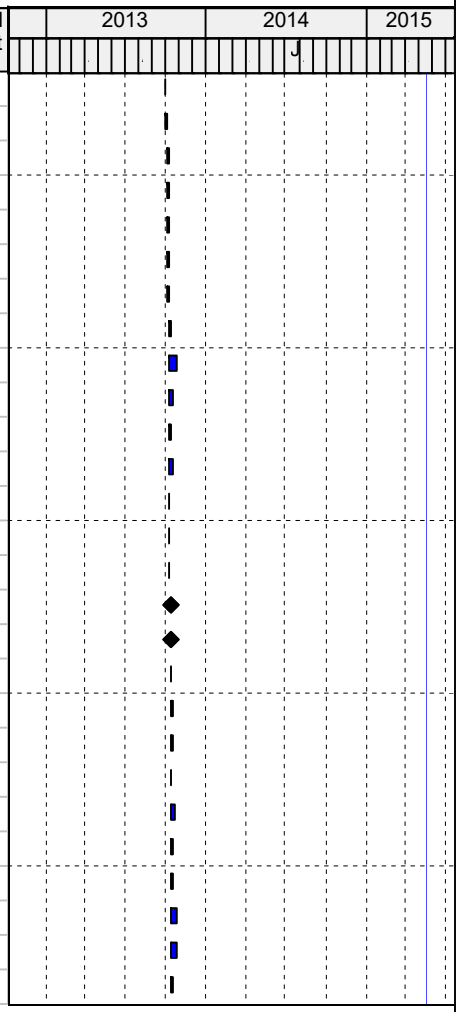



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P10A--2016 | Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2012 | Place / Finish Deck | 0 | 0 | 18-Oct-13 A | | |
| P7-2033 | Resteel/Shotcrete Walls | 3 | 0 | 18-Oct-13 A | 22-Oct-13 A | |
| P7-2014 | Stress Tendons | 1 | 0 | 21-Oct-13 A | 21-Oct-13 A | |
| P7-2016 | Strip / ReShore Deck | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2002 | FRP Columns Below | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P10B--2000 | FRP Shear Walls Below | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2004 | Shore / Form Deck | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P8-2012 | Place / Finish Deck P 8 & 9 and Core Walls | 0 | 0 | 25-Oct-13 A | | |
| P8-2014 | Stress Tendons | 1 | 0 | 28-Oct-13 A | 28-Oct-13 A | |
| P10B--2006 | MEP Rough In | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2008 | ReSteel / PT Cables | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2010 | Install Edgeform/Embeds | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P12--2002 | FRP Columns Below | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P12--2000 | Form/Resteel/Close Core Walls | 9 | 0 | 28-Oct-13 A | 07-Nov-13 A | |
| P12--2004 | Shore / Form Deck | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P8-2016 | Strip / ReShore Deck | 3 | 0 | 29-Oct-13 A | 31-Oct-13 A | |
| P11--2002 | FRP Columns Below | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P11--2004 | Shore / Form Deck | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P10B--2012 | Place / Finish Deck | 0 | 0 | 31-Oct-13 A | | |
| P10B--2014 | Stress Tendons | 1 | 0 | 01-Nov-13 A | 01-Nov-13 A | |
| P12--2006 | MEP Rough In | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12--2008 | ReSteel / PT Cables | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12--2010 | Install Edgeform/Embeds | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P10B--2016 | Strip / ReShore Deck | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2006 | MEP Rough In | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2008 | ReSteel / PT Cables | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |

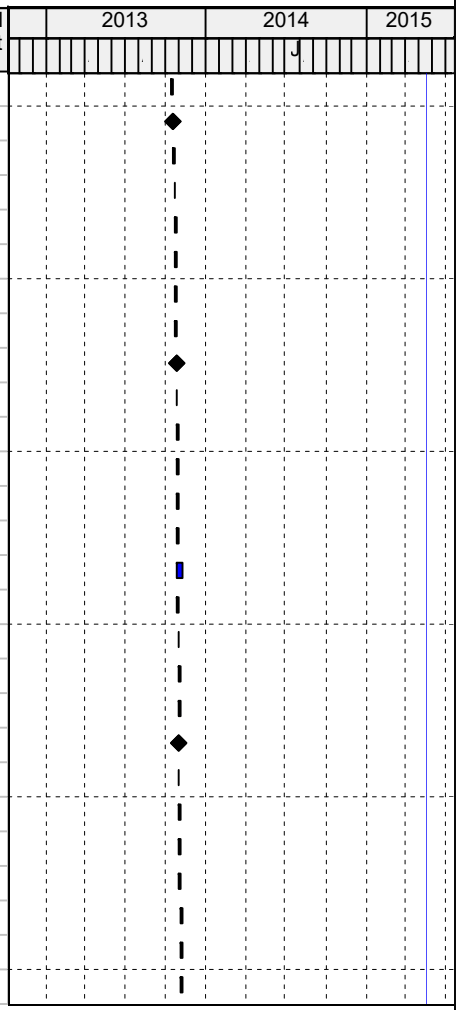



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P11–2010 | Install Edgeform/Embeds | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11–2012 | Place / Finish Deck | 0 | 0 | 07-Nov-13 A | | |
| P13–2002 | FRP Columns Below | 5 | 0 | 07-Nov-13 A | 14-Nov-13 A | |
| P13–2004 | Shore / Form Deck | 9 | 0 | 07-Nov-13 A | 28-Nov-13 A | |
| P11–2014 | Stress Tendons | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| P12–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 08-Nov-13 A | | |
| P11–2016 | Strip / ReShore Deck | 3 | 0 | 12-Nov-13 A | 14-Nov-13 A | |
| P12–2014 | Stress Tendons | 1 | 0 | 12-Nov-13 A | 12-Nov-13 A | |
| P14–2002 | FRP Columns Below | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P14–2000 | Form/Resteel/Close Core Walls | 8 | 0 | 19-Nov-13 A | 03-Dec-13 A | |
| P14–2004 | Shore / Form Deck | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P13A–2002 | FRP Columns Below | 5 | 0 | 21-Nov-13 A | 27-Nov-13 A | |
| P13A–2004 | Shore / Form Deck | 4 | 0 | 21-Nov-13 A | 26-Nov-13 A | |
| P13–2010 | Install Edgeform/Embeds | 5 | 0 | 22-Nov-13 A | 04-Dec-13 A | |
| P13–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2006 | MEP Rough In | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2010 | Install Edgeform/Embeds | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P13–2006 | MEP Rough In | 5 | 0 | 26-Nov-13 A | 03-Dec-13 A | |
| P13A–2006 | MEP Rough In | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2008 | ReSteel / PT Cables | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2010 | Install Edgeform/Embeds | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13–2012 | Place / Finish Deck | 0 | 0 | 02-Dec-13 A | | |
| P13A–2012 | Place / Finish Deck | 0 | 0 | 03-Dec-13 A | | |
| P14–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 04-Dec-13 A | | |
| P13–2014 | Stress Tendons | 1 | 0 | 05-Dec-13 A | 05-Dec-13 A | |
| P15–2002 | FRP Columns Below | 3 | 0 | 05-Dec-13 A | 09-Dec-13 A | |

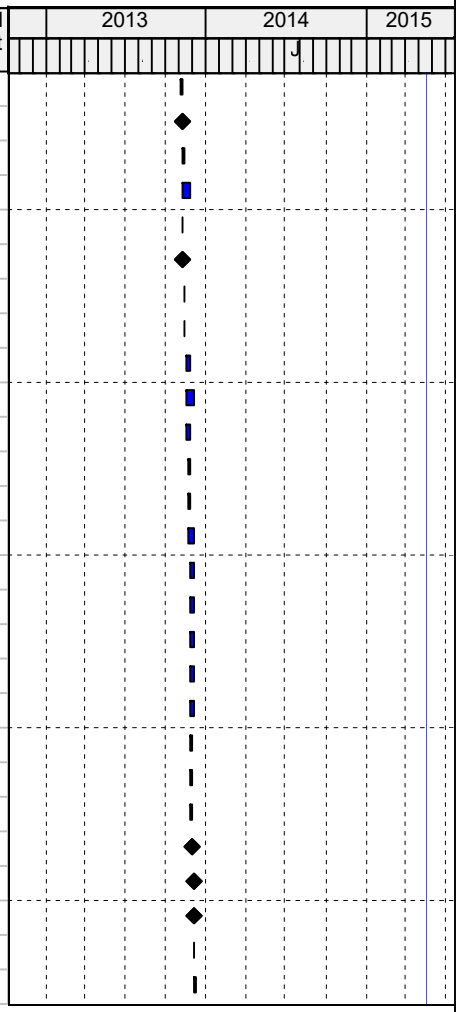



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P15–2000 | Jump/Resteel/Close Core | 9 | 0 | 05-Dec-13 A | 17-Dec-13 A | |
| P15–2004 | Shore / Form Deck | 5 | 0 | 05-Dec-13 A | 11-Dec-13 A | |
| P13–2016 | Strip / ReShore Deck | 3 | 0 | 06-Dec-13 A | 10-Dec-13 A | |
| P13A–2014 | Stress Tendons | 1 | 0 | 06-Dec-13 A | 06-Dec-13 A | |
| P14–2014 | Stress Tendons | 1 | 0 | 07-Dec-13 A | 07-Dec-13 A | |
| P15–2006 | MEP Rough In | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2008 | ReSteel / PT Cables | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2010 | Install Edgeform/Embeds | 3 | 0 | 11-Dec-13 A | 13-Dec-13 A | |
| P16-2002 | FRP Columns Below | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P16-2004 | Shore / Form Deck | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P15–2012 | Place / Finish Deck | 0 | 0 | 18-Dec-13 A | | |
| P15–2020 | Place Conc @ Core | 0 | 0 | 18-Dec-13 A | | |
| P16-2000 | Jump/Resteel/Close Core | 5 | 0 | 18-Dec-13 A | 24-Dec-13 A | |
| P16-2006 | MEP Rough In | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2008 | ReSteel / PT Cables | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2010 | Install Edgeform/Embeds | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P15–2014 | Stress Tendons | 1 | 0 | 21-Dec-13 A | 21-Dec-13 A | |
| P8-2018 | Remove Reshores | 2 | 0 | 23-Dec-13 A | 24-Dec-13 A | |
| P10A–2018 | Remove Reshores | 2 | 0 | 26-Dec-13 A | 27-Dec-13 A | |
| P16-2012 | Place / Finish Deck | 0 | 0 | 26-Dec-13 A | | |
| P16-2020 | Place Conc @ Core | 0 | 0 | 26-Dec-13 A | | |
| P17-2002 | FRP Columns Below | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P17-2000 | Jump/Resteel/Close Core | 7 | 0 | 27-Dec-13 A | 07-Jan-14 A | |
| P17-2004 | Shore / Form Deck | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P10B–2018 | Remove Reshores | 2 | 0 | 30-Dec-13 A | 31-Dec-13 A | |
| P16-2014 | Stress Tendons | 1 | 0 | 31-Dec-13 A | 31-Dec-13 A | |
| P5A-2018 | LL1 - Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |

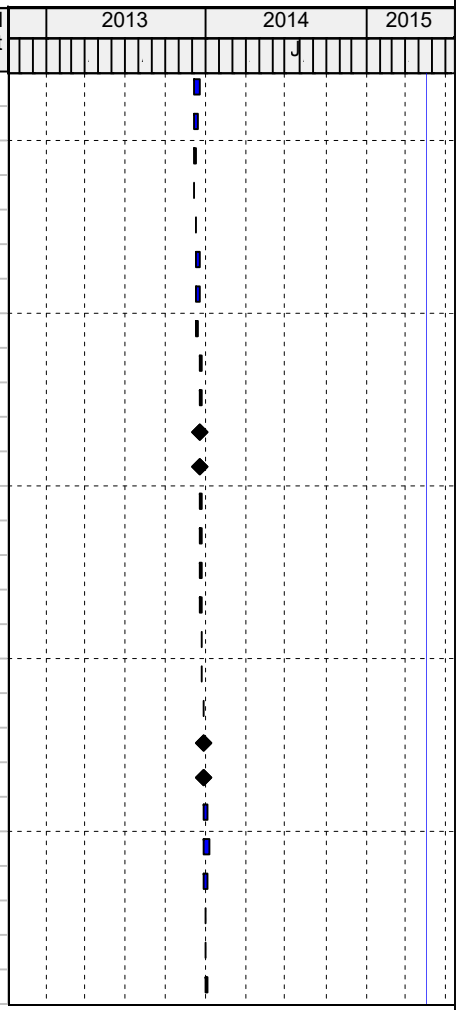



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P11–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P12–2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P17-2006 | MEP Rough In | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2008 | ReSteel / PT Cables | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2010 | Install Edgeform/Embeds | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P6-2018 | LL1 - Remove Reshores | 2 | 0 | 06-Jan-14 A | 07-Jan-14 A | |
| P5B-2018 | LL1 - Remove Reshores | 2 | 0 | 08-Jan-14 A | 09-Jan-14 A | |
| P17-2012 | Place / Finish Deck | 0 | 0 | 08-Jan-14 A | | |
| P17-2020 | Place Conc @ Core | 0 | 0 | 08-Jan-14 A | | |
| P18-2002 | FRP Columns Below | 5 | 0 | 09-Jan-14 A | 15-Jan-14 A | |
| P18-2000 | Jump/Resteel/Close Core | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P18-2004 | Shore / Form Deck | 3 | 0 | 09-Jan-14 A | 13-Jan-14 A | |
| LL2-2022R | MEP Rough In | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P7-2018 | Remove Reshores | 2 | 0 | 10-Jan-14 A | 13-Jan-14 A | |
| P17-2014 | Stress Tendons | 1 | 0 | 11-Jan-14 A | 11-Jan-14 A | |
| P13–2018 | Remove Reshores | 2 | 0 | 13-Jan-14 A | 14-Jan-14 A | |
| P13A–2018 | Remove Reshores | 2 | 0 | 15-Jan-14 A | 16-Jan-14 A | |
| WEA-2012 | WIND IMPACT | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| P18-2006 | MEP Rough In | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2008 | ReSteel / PT Cables | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2010 | Install Edgeform/Embeds | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2012 | Place / Finish Deck | 0 | 0 | 22-Jan-14 A | | |
| P18-2020 | Place Conc @ Core | 0 | 0 | 22-Jan-14 A | | |
| P19-2002 | FRP Columns Below | 5 | 0 | 23-Jan-14 A | 29-Jan-14 A | |
| P19-2000 | Jump/Resteel/Close Core | 4 | 0 | 23-Jan-14 A | 28-Jan-14 A | |
| P19-2004 | Shore / Form Deck | 3 | 0 | 23-Jan-14 A | 27-Jan-14 A | |
| P18-2014 | Stress Tendons | 1 | 0 | 25-Jan-14 A | 25-Jan-14 A | |

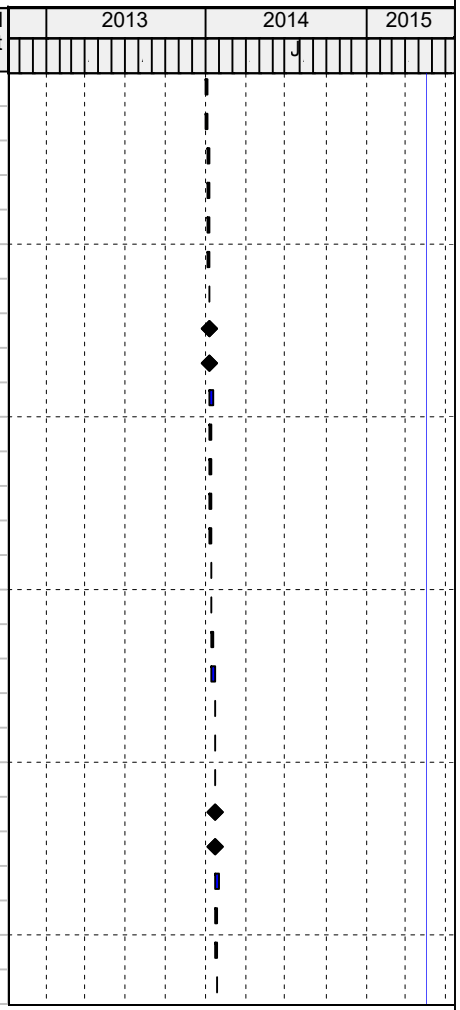


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P14–2018 | Remove Reshores | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2006 | MEP Rough In | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2008 | ReSteel / PT Cables | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2010 | Install Edgeform/Embeds | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2012 | Place / Finish Deck | 0 | 0 | 29-Jan-14 A | | |
| P19-2020 | Place Conc @ Core | 0 | 0 | 29-Jan-14 A | | |
| P20-2002 | FRP Columns Below | 5 | 0 | 30-Jan-14 A | 05-Feb-14 A | |
| P20-2000 | Jump/Resteel/Close Core | 9 | 0 | 30-Jan-14 A | 11-Feb-14 A | |
| P20-2004 | Shore / Form Deck | 6 | 0 | 30-Jan-14 A | 10-Feb-14 A | |
| P19-2014 | Stress Tendons | 1 | 0 | 01-Feb-14 A | 01-Feb-14 A | |
| P13A–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P14–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P15–2016 | Strip / ReShore Deck | 3 | 0 | 06-Feb-14 A | 10-Feb-14 A | |
| P20-2006 | MEP Rough In | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2008 | ReSteel / PT Cables | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2010 | Install Edgeform/Embeds | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| L03-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 06-Feb-14 A | 12-Feb-14 A | |
| P16-2016 | Strip / ReShore Deck | 3 | 0 | 10-Feb-14 A | 12-Feb-14 A | |
| L04-2018 | Remove Reshores | 2 | 0 | 10-Feb-14 A | 11-Feb-14 A | |
| L03-2018 | Remove Reshores | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| P17-2016 | Strip / ReShore Deck | 3 | 0 | 12-Feb-14 A | 14-Feb-14 A | |
| P20-2012 | Place / Finish Deck | 0 | 0 | 12-Feb-14 A | | |
| P20-2020 | Place Conc @ Core | 0 | 0 | 12-Feb-14 A | | |
| L04-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-Feb-14 A | 18-Feb-14 A | |
| P12–2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P18-2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P21-2002 | FRP Columns Below | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |

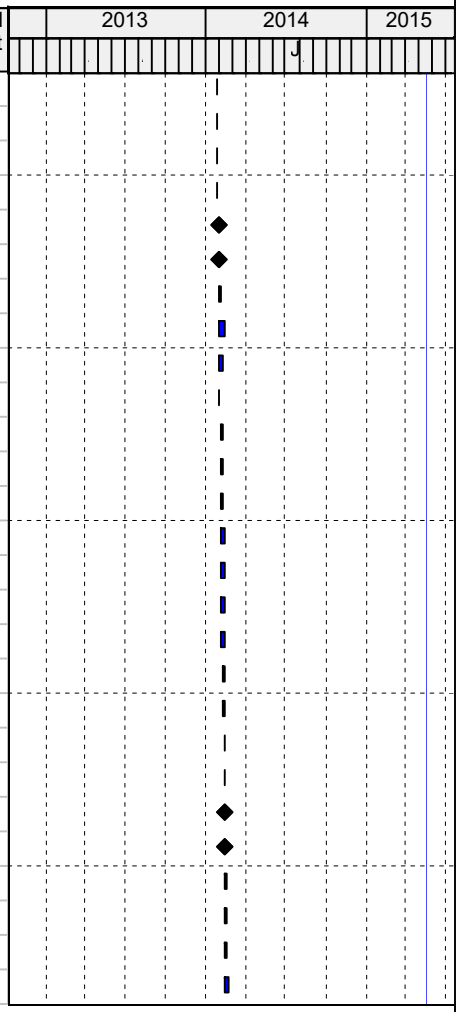



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P21-2000 | Jump/Resteel/Close Core | 4 | 0 | 13-Feb-14 A | 18-Feb-14 A | |
| P21-2004 | Shore / Form Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P19-2016 | Strip / ReShore Deck | 3 | 0 | 14-Feb-14 A | 18-Feb-14 A | |
| P20-2014 | Stress Tendons | 1 | 0 | 15-Feb-14 A | 15-Feb-14 A | |
| P21-2006 | MEP Rough In | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2008 | ReSteel / PT Cables | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P20-2016 | Strip / ReShore Deck | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| L05-2018 | Remove Reshores | 2 | 0 | 18-Feb-14 A | 19-Feb-14 A | |
| P21-2012 | Place / Finish Deck | 0 | 0 | 19-Feb-14 A | | |
| P21-2020 | Place Conc @ Core | 0 | 0 | 19-Feb-14 A | | |
| P22-2002 | FRP Columns Below | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P22-2000 | Jump/Resteel/Close Core | 4 | 0 | 20-Feb-14 A | 25-Feb-14 A | |
| P22-2004 | Shore / Form Deck | 3 | 0 | 20-Feb-14 A | 24-Feb-14 A | |
| L05-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P21-2014 | Stress Tendons | 1 | 0 | 22-Feb-14 A | 22-Feb-14 A | |
| P21-2016 | Strip / ReShore Deck | 3 | 0 | 24-Feb-14 A | 26-Feb-14 A | |
| P22-2006 | MEP Rough In | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2008 | ReSteel / PT Cables | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| L06-2018 | Remove Reshores | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| P22-2012 | Place / Finish Deck | 0 | 0 | 26-Feb-14 A | | |
| P22-2020 | Place Conc @ Core | 0 | 0 | 26-Feb-14 A | | |
| P23-2002 | FRP Columns Below | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2000 | Jump/Resteel/Close Core | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2004 | Shore / Form Deck | 3 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2006 | MEP Rough In | 2 | 0 | 01-Mar-14 A | 03-Mar-14 A | |

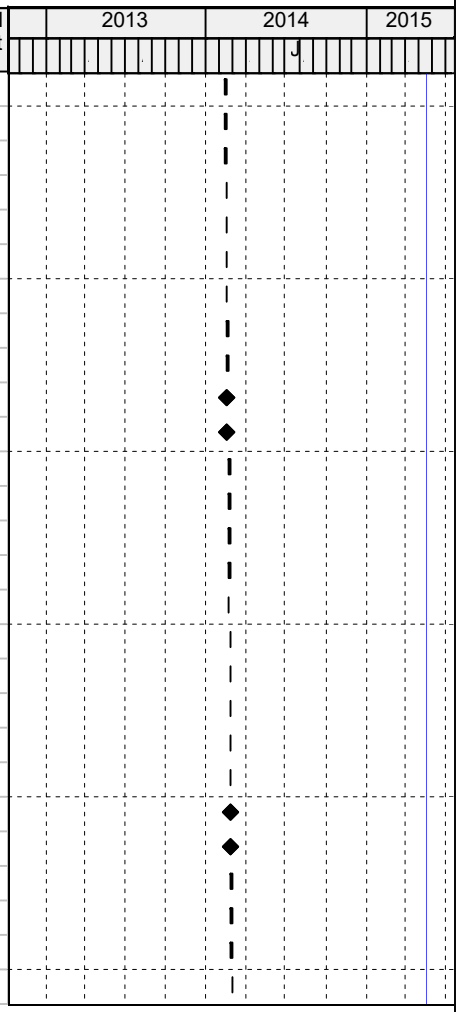



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P22-2014 | Stress Tendons | 1 | 0 | 01-Mar-14 A | 01-Mar-14 A | |
| P23-2008 | ReSteel / PT Cables | 2 | 0 | 03-Mar-14 A | 04-Mar-14 A | |
| P22-2016 | Strip / ReShore Deck | 3 | 0 | 04-Mar-14 A | 10-Mar-14 A | |
| P23-2010 | Install Edgeform/Embeds | 2 | 0 | 04-Mar-14 A | 04-Mar-14 A | |
| L07-2018 | Remove Reshores | 2 | 0 | 04-Mar-14 A | 05-Mar-14 A | |
| P23-2012 | Place / Finish Deck | 0 | 0 | 05-Mar-14 A | | |
| P23-2020 | Place Conc @ Core | 0 | 0 | 05-Mar-14 A | | |
| P24-2002 | FRP Columns Below | 5 | 0 | 05-Mar-14 A | 07-Mar-14 A | |
| P24-2004 | Shore / Form Deck | 3 | 0 | 06-Mar-14 A | 10-Mar-14 A | |
| P24-2000 | Jump/Resteel/Close Core | 4 | 0 | 08-Mar-14 A | 10-Mar-14 A | |
| P23-2014 | Stress Tendons | 1 | 0 | 10-Mar-14 A | 10-Mar-14 A | |
| P24-2008 | ReSteel / PT Cables | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P24-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P23-2016 | Strip / ReShore Deck | 3 | 0 | 11-Mar-14 A | 17-Mar-14 A | |
| P24-2006 | MEP Rough In | 2 | 0 | 11-Mar-14 A | 11-Mar-14 A | |
| P25-2002 | FRP Columns Below | 5 | 0 | 11-Mar-14 A | 13-Mar-14 A | |
| L08-2018 | Remove Reshores | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| P24-2012 | Place / Finish Deck | 0 | 0 | 12-Mar-14 A | | |
| P24-2020 | Place Conc @ Core | 0 | 0 | 12-Mar-14 A | | |
| P25-2004 | Shore / Form Deck | 3 | 0 | 13-Mar-14 A | 17-Mar-14 A | |
| P25-2000 | Jump/Resteel/Close Core | 4 | 0 | 15-Mar-14 A | 17-Mar-14 A | |
| P24-2014 | Stress Tendons | 1 | 0 | 17-Mar-14 A | 17-Mar-14 A | |
| P25-2006 | MEP Rough In | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2008 | ReSteel / PT Cables | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| L06-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 18-Mar-14 A | 20-Mar-14 A | |
| L09-2018 | Remove Reshores | 2 | 0 | 18-Mar-14 A | 19-Mar-14 A | |

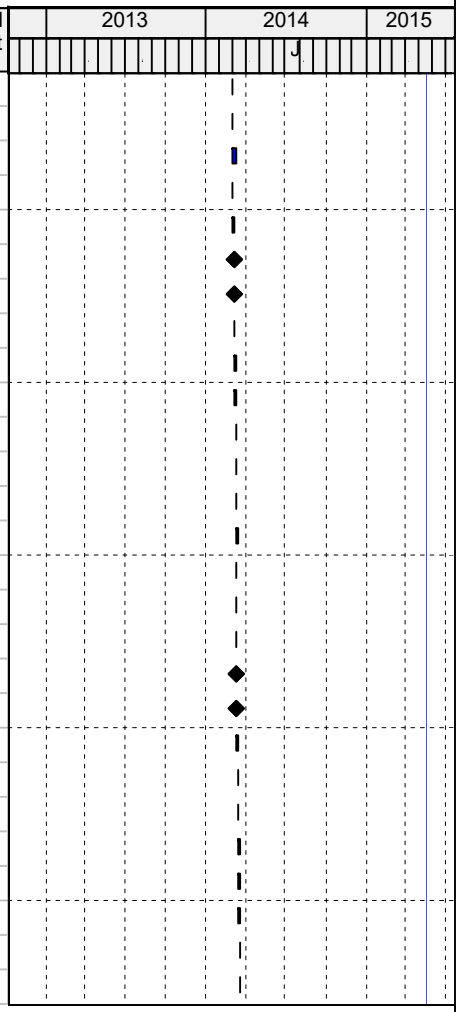



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P26-2002 | FRP Columns Below | 5 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| P25-2012 | Place / Finish Deck | 0 | 0 | 19-Mar-14 A | | |
| P25-2020 | Place Conc @ Core | 0 | 0 | 19-Mar-14 A | | |
| P26-2004 | Shore / Form Deck | 3 | 0 | 20-Mar-14 A | 24-Mar-14 A | |
| L07-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 21-Mar-14 A | 25-Mar-14 A | |
| P26-2000 | Jump/Resteel/Close Core | 4 | 0 | 22-Mar-14 A | 24-Mar-14 A | |
| P26-2006 | MEP Rough In | 2 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P26-2008 | ReSteel / PT Cables | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P26-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P25-2014 | Stress Tendons | 1 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P27-2002 | FRP Columns Below | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| P26-2012 | Place / Finish Deck | 0 | 0 | 26-Mar-14 A | | |
| P26-2020 | Place Conc @ Core | 0 | 0 | 26-Mar-14 A | | |
| L08-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 26-Mar-14 A | 28-Mar-14 A | |
| L10-2018 | Remove Reshores | 2 | 0 | 26-Mar-14 A | 27-Mar-14 A | |
| P27-2004 | Shore / Form Deck | 3 | 0 | 27-Mar-14 A | 31-Mar-14 A | |
| P27-2000 | Jump/Resteel/Close Core | 4 | 0 | 29-Mar-14 A | 31-Mar-14 A | |
| P27-2006 | MEP Rough In | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2008 | ReSteel / PT Cables | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2010 | Install Edgeform/Embeds | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P26-2014 | Stress Tendons | 1 | 0 | 31-Mar-14 A | 31-Mar-14 A | |
| L09-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 31-Mar-14 A | 02-Apr-14 A | |
| P24-2016 | Strip / ReShore Deck | 3 | 0 | 01-Apr-14 A | 07-Apr-14 A | |
| L11-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 02-Apr-14 A | |
| L12-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 03-Apr-14 A | |
| P27-2012 | Place / Finish Deck | 0 | 0 | 02-Apr-14 A | | |
| P27-2020 | Place Conc @ Core | 0 | 0 | 02-Apr-14 A | | |

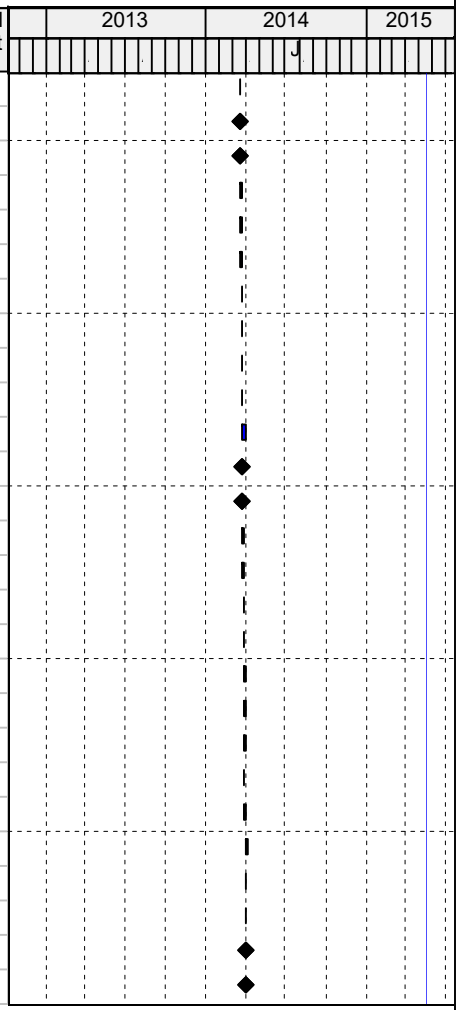



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P28-2002 | FRP Columns Below | 5 | 0 | 02-Apr-14 A | 04-Apr-14 A | |
| P28-2004 | Shore / Form Deck | 4 | 0 | 03-Apr-14 A | 08-Apr-14 A | |
| L10-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| P27-2014 | Stress Tendons | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| P25-2016 | Strip / ReShore Deck | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L14-2018 | Remove Reshores | 2 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| P28-2000 | Jump/Resteel/Close Core | 7 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| P28-2006 | MEP Rough In | 4 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2008 | ReSteel / PT Cables | 4 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Apr-14 A | 11-Apr-14 A | |
| L12-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| P28-2012 | Place / Finish Deck | 0 | 0 | 14-Apr-14 A | | |
| P28-2020 | Place Conc @ Core | 0 | 0 | 14-Apr-14 A | | |
| P29-2002 | FRP Columns Above Roof Deck | 3 | 0 | 14-Apr-14 A | 18-Apr-14 A | |
| P26-2016 | Strip / ReShore Deck | 3 | 0 | 14-Apr-14 A | 17-Apr-14 A | |
| L14-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-Apr-14 A | 18-Apr-14 A | |
| P28-2014 | Stress Tendons | 1 | 0 | 17-Apr-14 A | 17-Apr-14 A | |
| P29-2000 | Strip Core | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| P27-2016 | Strip / ReShore Deck | 3 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L15-2018 | Remove Reshores | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| P28-2016 | Strip / ReShore Deck | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L15-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L16-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-May-14 A | 19-May-14 A | |
| L16-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2019 | Grind Ceiling for Skim Coat | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |

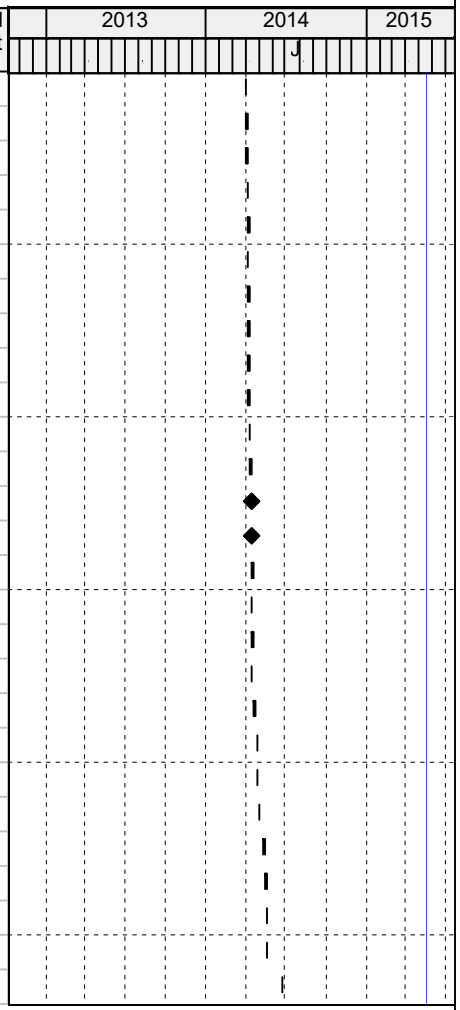



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Ballroom Catwalk & Roof** | | | | | | |
| PC-2100 | Erect Structural Steel @ Porte Cochere | 3 | 0 | 30-Jan-14 A | 03-Feb-14 A | |
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 7 | 0 | 07-Feb-14 A | 17-Feb-14 A | |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| PC-2102 | Metal Decking @ Porte Cochere/ Roof | 2 | 0 | 17-Apr-14 A | 18-Apr-14 A | |
| BR-2112 | BR - Fireproofing @ Structural Steel | 2 | 0 | 27-May-14 A | 30-May-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Mech Penthouse** | | | | | | |
| PH-8706 | Set Mech Equipment @ Tower Roof | 3 | 0 | 22-May-14 A | 28-May-14 A | |
| PH-8708 | Set Equipment @ Penthouse | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| PH-8700 | PH - Structural Steel and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| **Vertical Circulation** | | | | | | |
| **Stairs** | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 25-Nov-13 A | 26-Nov-13 A | |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 27-Nov-13 A | 03-Dec-13 A | |
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 04-Dec-13 A | 05-Dec-13 A | |
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 06-Dec-13 A | 09-Dec-13 A | |
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 2 | 0 | 03-Feb-14 A | 04-Feb-14 A | |
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 2 | 0 | 06-Feb-14 A | 07-Feb-14 A | |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 2 | 0 | 07-Feb-14 A | 07-Feb-14 A | |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 2 | 0 | 07-Feb-14 A | 10-Feb-14 A | |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 2 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 2 | 0 | 06-Mar-14 A | 07-Mar-14 A | |

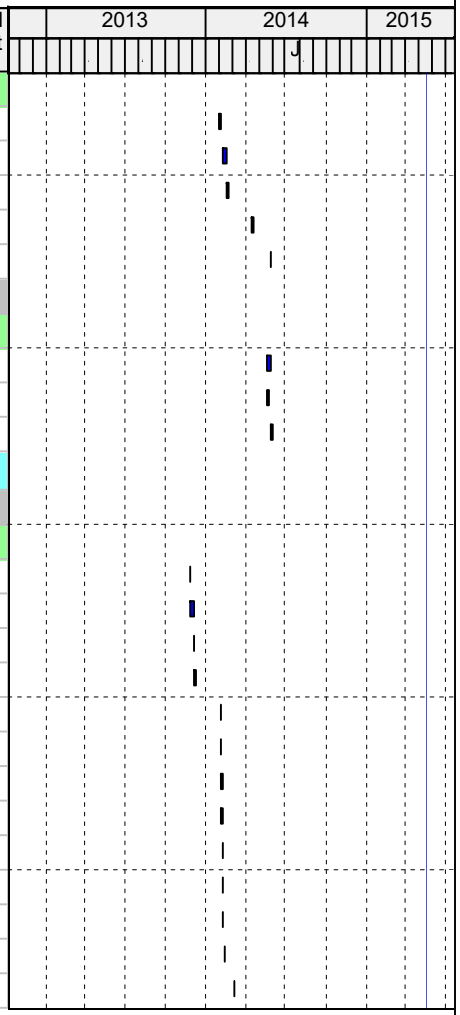



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 2 | 0 | 07-Mar-14 A | 10-Mar-14 A | |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 2 | 0 | 13-Mar-14 A | 14-Mar-14 A | |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 2 | 0 | 08-Apr-14 A | 21-Apr-14 A | |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| S1-4040 | Stair 1 - Set Mtl Stairs / Railings L18 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 10-Dec-13 A | 11-Dec-13 A | |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 12-Dec-13 A | 13-Dec-13 A | |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 16-Dec-13 A | 17-Dec-13 A | |
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 18-Dec-13 A | 19-Dec-13 A | |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 2 | 0 | 12-Feb-14 A | 13-Feb-14 A | |
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 2 | 0 | 13-Feb-14 A | 13-Feb-14 A | |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 2 | 0 | 13-Feb-14 A | 14-Feb-14 A | |
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 2 | 0 | 19-Feb-14 A | 20-Feb-14 A | |
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 2 | 0 | 21-Feb-14 A | 24-Feb-14 A | |
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 2 | 0 | 19-Mar-14 A | 20-Mar-14 A | |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 2 | 0 | 21-Mar-14 A | 22-Mar-14 A | |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 2 | 0 | 14-May-14 A | 15-May-14 A | |

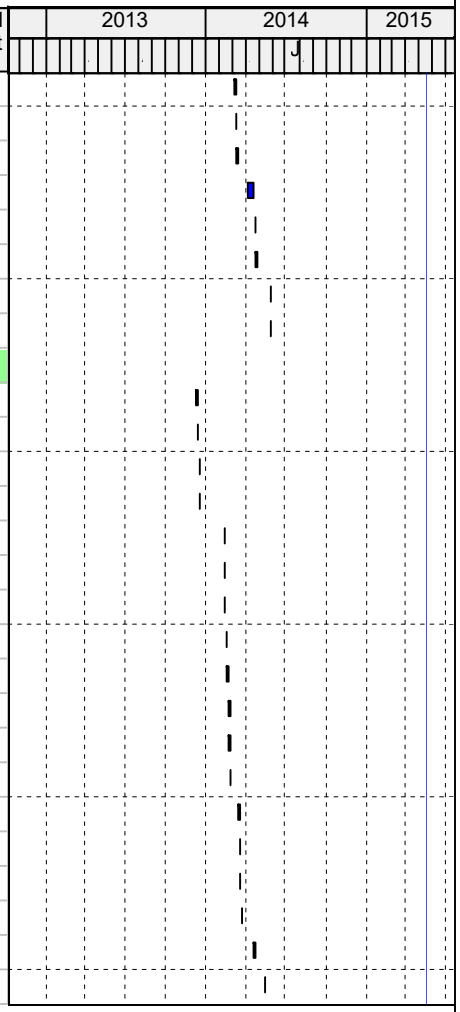



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 2 | 0 | 16-May-14 A | 19-May-14 A | |
| S2-4038 | Stair 2 - Set Mtl Stairs / Railings L17 | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - Set Metal Stairs / Railings LL2 | 6 | 0 | 05-Mar-14 A | 20-Mar-14 A | |
| S3-4002 | Stair 3 - Set Metal Stairs / Railings LL1 | 6 | 0 | 17-Mar-14 A | 21-Mar-14 A | |
| S3-4004 | Stair 3 - Paint walls & railings | 4 | 0 | 04-May-15 A | 11-May-15 A | |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |
| S4-4000 | Stair 4 - Set Metal Stairs / Railings LL2 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4002 | Stair 4 - Set Metal Stairs / Railings LL1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4004 | Stair 4 -Set Metal Stairs / Railings L1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4006 | Stair 4 - Paint walls & railings | 4 | 0 | 28-Apr-15 A | 01-May-15 A | |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |
| S6-4000 | Stair 6 - Set Metal Stairs / Railings | 5 | 0 | 25-Jun-14 A | 01-Jul-14 A | |
| S6-4002 | Stair 6 - Paint walls & railings | 2 | 0 | 01-Apr-15 A | 03-Apr-15 A | |
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes (DE | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a -Set Metal Stairs / Railings L1 | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| S4a-4002 | Stair 4a - Paint walls & railings | 2 | 0 | 04-May-15 A | 08-May-15 A | |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 07-Jun-13 A | | |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 0 | 17-Jun-13 A | 21-Jun-13 A | |
| EL-1004 | Elev - Submittal Approval | 21 | 0 | 21-Jun-13 A | 01-Jan-14 A | |
| EL-1006 | Elev - Release to Manufacturing | 14 | 0 | 02-Jan-14 A | 15-Jan-14 A | |

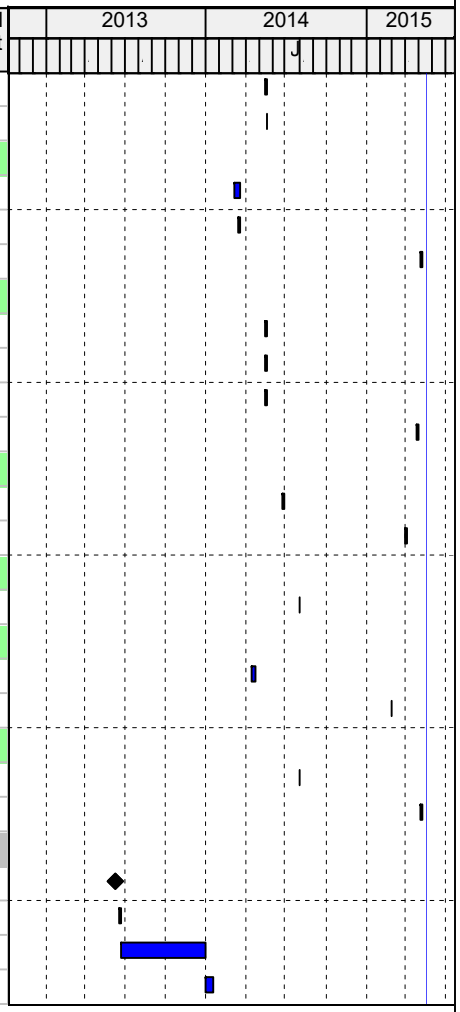



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-1008 | Elev - Fabrication (Engineered Geared) | 95 | 0 | 16-Jan-14 A | 14-Jun-14 A | |
| EL-1010 | Elev - Machines delivered | 1 | 0 | 12-May-14 A | 12-May-14 A | |
| EL-1011 | Elev - Elevator Machines Flown & Set At Top Of Hoist | 5 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5016 | Elev 5 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-1216 | Elev 1&2 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-3416 | Elev 3&4 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-1202 | Elev 1&2 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-3402 | Elev 3&4 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-5018 | Elev 5 - Set Hoistway Machines | 3 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| EL-1218 | Elev 1&2 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-3418 | Elev 3&4 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-1200 | Elev 1&2 - Hoistway Clear & Ready (GC) | 0 | 0 | 20-Jun-14 A | | |
| EL-1204 | Elev 1&2 - Install Rails & Brackets | 17 | 0 | 23-Jun-14 A | 15-Jul-14 A | |
| EL-3400 | Elev 3&4 - Hoistway Clear & Ready (GC) | 0 | 0 | 23-Jun-14 A | | |
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 24-Jun-14 A | | |
| EL-1206 | Elev 1&2 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Jul-14 A | |
| EL-1207 | Elev 1&2 - Install Pit Equipment/Car Sling/CWT Fram | 3 | 0 | 15-Jul-14 A | 01-Aug-14 A | |
| EL-1208 | Elev 1&2 - Install MHoist & Cable | 5 | 0 | 16-Jul-14 A | 24-Jul-14 A | |
| EL-3407 | Elev 3&4 - Install Pit Equipment/Car Sling/CWT Fram | 5 | 0 | 16-Jul-14 A | 06-Aug-14 A | |
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 21-Jul-14 A | | |
| EL-5004 | Elev 5 - Install Rails & Brackets | 13 | 0 | 21-Jul-14 A | 11-Aug-14 A | |
| EL-3404 | Elev 3&4 - Install Rails & Brackets | 18 | 0 | 23-Jul-14 A | 04-Aug-14 A | |
| EL-3406 | Elev 3&4 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 28-Jul-14 A | |
| EL-3408 | Elev 3&4 - Install Hoist & Cable | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| EL-5007 | Elev 5 - Install Pit Equipment/Car Sling/CWT Frame/V | 5 | 0 | 12-Aug-14 A | 15-Aug-14 A | |

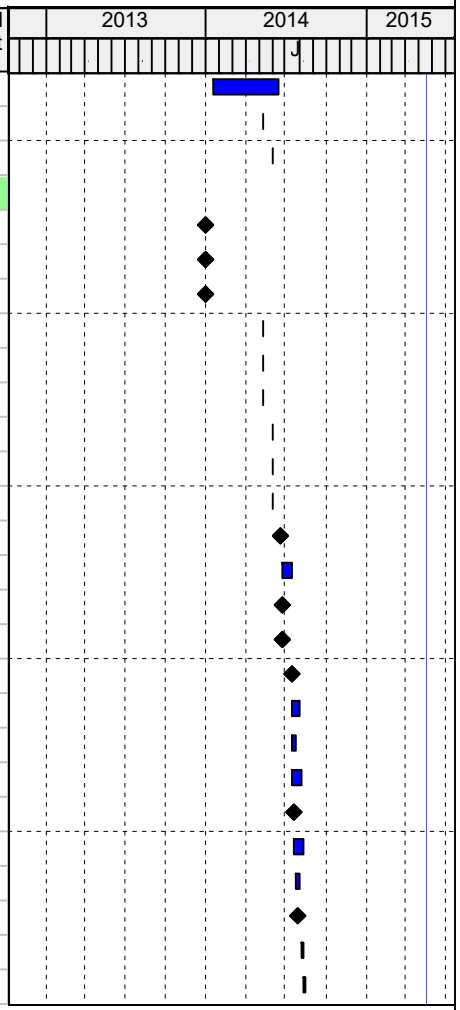



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-1210 | Elev 1&2 - Install Entrances/Doors/Fixtures/Fascia | 19 | 0 | 14-Aug-14 A | 22-Sep-14 A | |
| EL-3410 | Elev 3&4 - Install Entrances/Doors/Fixtures/Fascia | 30 | 0 | 14-Aug-14 A | 02-Oct-14 A | |
| EL-5006 | Elev 5 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Aug-14 A | |
| EL-5008 | Elev 5 - Install MHoist & Cable | 4 | 0 | 18-Aug-14 A | 20-Aug-14 A | |
| EL-5010 | Elev 5 - Install Entrances/Doors/Fixtures/Fascia | 21 | 0 | 21-Aug-14 A | 26-Sep-14 A | |
| EL-1212 | Elev 1&2 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 22-Sep-14 A | 13-Oct-14 A | |
| EL-5012 | Elev 5 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 26-Sep-14 A | 16-Oct-14 A | |
| EL-3412 | Elev 3&4 - Install Hoistway Equipment/Pipe & Wire | 23 | 0 | 03-Oct-14 A | 03-Nov-14 A | |
| EL-1214 | Elev 1&2 - Install Cab/Wiring/Door Operator(s) | 11 | 0 | 14-Oct-14 A | 28-Oct-14 A | |
| EL-5014 | Elev 5 - Install Cab/Wiring/Door Operator(s) | 7 | 0 | 17-Oct-14 A | 27-Oct-14 A | |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 1 | 0 | 24-Oct-14 A | 24-Oct-14 A | |
| EL-6016 | Elev 6 - Hoistway Walls Complete (GC) | 0 | 0 | | 24-Oct-14 A | |
| EL-6004 | Elev 6 - Install Cylinders/Rails & Brackets | 4 | 0 | 27-Oct-14 A | 30-Oct-14 A | |
| EL-5022 | Elev 5 - Adjust | 5 | 0 | 28-Oct-14 A | 03-Nov-14 A | |
| EL-1222 | Elev 1&2 - Adjust | 5 | 0 | 29-Oct-14 A | 04-Nov-14 A | |
| EL-6006 | Elev 6 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 30-Oct-14 A | |
| EL-6007 | Elev 6 - Install Pit Equipment/Car Sling | 2 | 0 | 31-Oct-14 A | 03-Nov-14 A | |
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| EL-3414 | Elev 3&4 - Install Cab/Wiring/Door Operator(s) | 10 | 0 | 04-Nov-14 A | 17-Nov-14 A | |
| EL-6018 | Elev 6 - Install Machine Room Equipment | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| EL-1224 | Elev 1&2 - Clean / Paint / Punchlist | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| EL-5026 | Elev 5 - Inspections | 7 | 0 | 13-Nov-14 A | 14-Nov-14 A | |
| EL-3422 | Elev 3&4 - Adjust | 8 | 0 | 18-Nov-14 A | 20-Nov-14 A | |
| EL-6012 | Elev 6 - Install hoistway rails & divider beams | 2 | 0 | 20-Nov-14 A | 21-Nov-14 A | |
| EL-6010 | Elev 6 - Install elevator fronts/rears | 9 | 0 | 09-Dec-14 A | 24-Dec-14 A | |
| EL-6014 | Elev 6 - Cab build-out | 5 | 0 | 15-Dec-14 A | 30-Jan-15 A | |
| EL-6022 | Elev 6 - Final cleaning at EMR | 4 | 0 | 25-Feb-15 A | 27-Feb-15 A | |

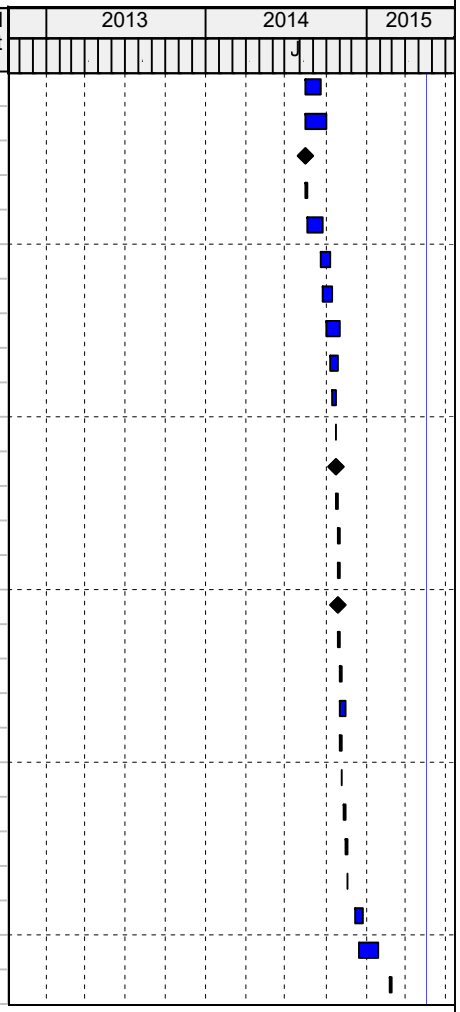


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-1226 | Elev 1&2 - CoB/L&I Inspections (for FF&E use) | 3 | 0 | 04-Mar-15 A | 06-Mar-15 A | |
| EL-3424 | Elev 3&4 - Walsh/TKE pre-inspection | 6 | 0 | 27-Mar-15 A | 27-Mar-15 A | |
| EL-6024 | Elev 6 - Walsh/TKE pre-inspection | 2 | 0 | 13-Apr-15 A | 14-Apr-15 A | |
| EL-3426 | Elev 3&4 - CoB/L&I Inspections (Final) | 2 | 2 | 19-May-15* | 20-May-15 | 7 |
| EL-6026 | Elev 6 - CoB/L&I Inspections (Final) | 2 | 2 | 19-May-15 | 20-May-15 | 7 |
| **Exterior Shell** | | | | | | |
| **Elevations** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2** | | | | | | |
| L3D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Feb-14 A | 12-Feb-14 A | |
| L3-5308 | L3- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 17-Feb-14 A | 21-Feb-14 A | |
| L4D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Feb-14 A | 19-Feb-14 A | |
| L4-5308 | L4- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Feb-14 A | 28-Feb-14 A | |
| L5D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Feb-14 A | 26-Feb-14 A | |
| L5-5308 | L5- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 03-Mar-14 A | 07-Mar-14 A | |
| L6D5308 | Deliver/Stock Wall Panels | 1 | 0 | 05-Mar-14 A | 05-Mar-14 A | |
| L6-5308 | L6- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L7-5308 | L7- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L7D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Mar-14 A | 12-Mar-14 A | |
| L8D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Mar-14 A | 19-Mar-14 A | |
| L8-5308 | L8- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Mar-14 A | 28-Mar-14 A | |
| L9D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L9-5308 | L9- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 31-Mar-14 A | 07-Apr-14 A | |
| 10D5308 | Deliver/Stock Wall Panels | 1 | 0 | 02-Apr-14 A | 02-Apr-14 A | |
| L10-5308 | L10- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 07-Apr-14 A | 11-Apr-14 A | |
| 11D5308 | Deliver/Stock Wall Panels | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L11-5308 | L11- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 11-Apr-14 A | 18-Apr-14 A | |

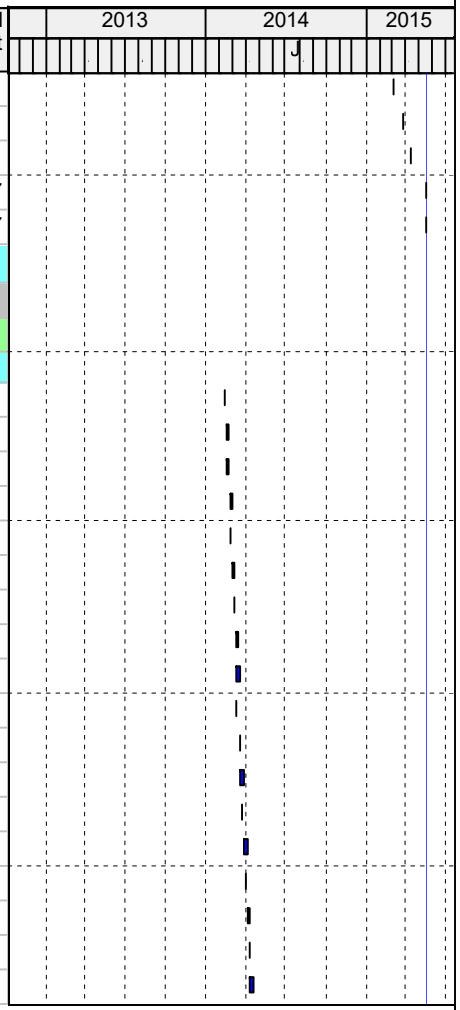



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| 12D5308 | Deliver/Stock Wall Panels | 1 | 0 | 16-Apr-14 A | 16-Apr-14 A | |
| L12-5308 | L12- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Apr-14 A | 25-Apr-14 A | |
| 14D5308 | Deliver/Stock Wall Panels | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L14-5308 | L14 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Apr-14 A | 01-May-14 A | |
| 15D5308 | Deliver/Stock Wall Panels | 1 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L15-5308 | L15 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| 16D5308 | Deliver/Stock Wall Panels | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L16-5308 | L16- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| 17D5308 | Deliver/Stock Wall Panels | 1 | 0 | 14-May-14 A | 14-May-14 A | |
| L17-5308 | L17 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 20-May-14 A | 11-Jun-14 A | |
| LL2-5308 | LL2 Thru L4 - Support Frame/Sheathing for Metal Wa | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL1-5308 | LL1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| L1-5308 | L1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| **Level 1** | | | | | | |
| L3-5102 | L3- Storefront Frames | 7 | 0 | 18-Aug-14 A | 29-Sep-14 A | |
| L1-5102 | L1 - Storefront Frames (excl. Main Entry Facade) | 8 | 0 | 02-Sep-14 A | 11-Sep-14 A | |
| L1-5104 | L1 - Storefront Glazing (excl. Main Entry Facade) | 4 | 0 | 19-Sep-14 A | 24-Sep-14 A | |
| EP-5110 | L1 - Revolving Doors | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L3-5104 | L3 - Storefront Glazing | 3 | 0 | 30-Sep-14 A | 03-Oct-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Levels 3-4** | | | | | | |
| L3-5130 | L3 - Install Punch Windows | 5 | 0 | 24-Feb-14 A | 10-Mar-14 A | |
| L4-5130 | L4 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 12-Mar-14 A | |
| L5-5130 | L5 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L6-5130 | L6- Install Punch Windows | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L7-5130 | L7 - Install Punch Windows | 5 | 0 | 18-Mar-14 A | 21-Mar-14 A | |
| L8-5130 | L8 - Install Punch Windows | 5 | 0 | 24-Mar-14 A | 28-Mar-14 A | |

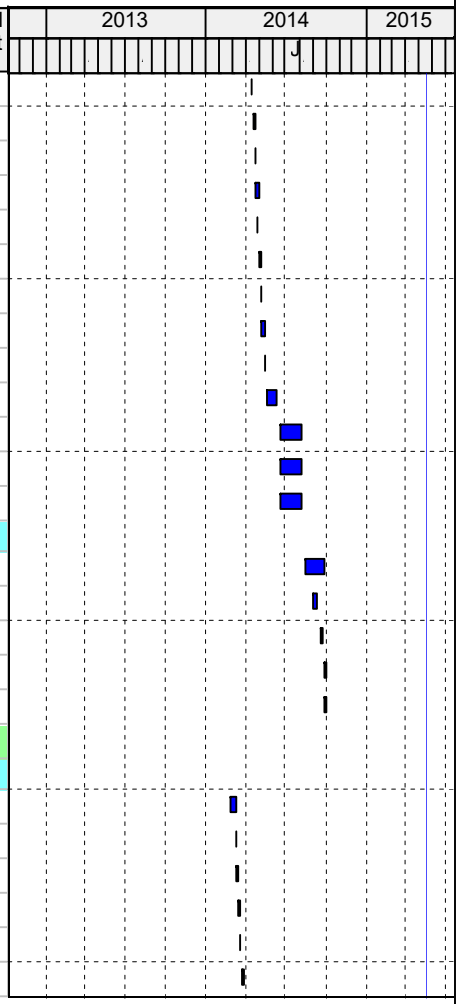


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L9-5130 | L9 - Install Punch Windows | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L10-5130 | L10 - Install Punch Windows | 5 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-5130 | L11 - Install Punch Windows | 5 | 0 | 14-Apr-14 A | 21-Apr-14 A | |
| L12-5130 | L12 - Install Punch Windows | 5 | 0 | 22-Apr-14 A | 25-Apr-14 A | |
| L14-5130 | L14 - Install Punch Windows | 5 | 0 | 28-Apr-14 A | 05-May-14 A | |
| L15-5130 | L15 - Install Punch Windows | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| L16-5130 | L16 - Install Punch Windows | 5 | 0 | 12-May-14 A | 20-May-14 A | |
| L17-5130 | L17 - Install Punch Windows | 5 | 0 | 27-May-14 A | 16-Jun-14 A | |
| Roofs | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| RF-4026 | L1 - City Park - Protection Board | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| **Pool Membrane - (elev 18')** | | | | | | |
| RF-4034 | Pool - Install plumbing | 3 | 0 | 20-Oct-14 A | 22-Oct-14 A | |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |
| RF-4010 | AR - Set Mechanical Equipment | 5 | 0 | 10-Jun-14 A | 12-Jun-14 A | |
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 10 | 0 | 04-Aug-14 A | 27-Aug-14 A | |
| RF-4012 | L2.5 Horseshoe - Install corrugated metal panels | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 8 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |
| PC-4008 | RF - Entry / Porte Cochere Roofing System | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | RF - Upper Ballroom Roofing System | 3 | 0 | 28-Jul-14 A | 31-Jul-14 A | |
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 4 | 0 | 31-Jul-14 A | 04-Aug-14 A | |

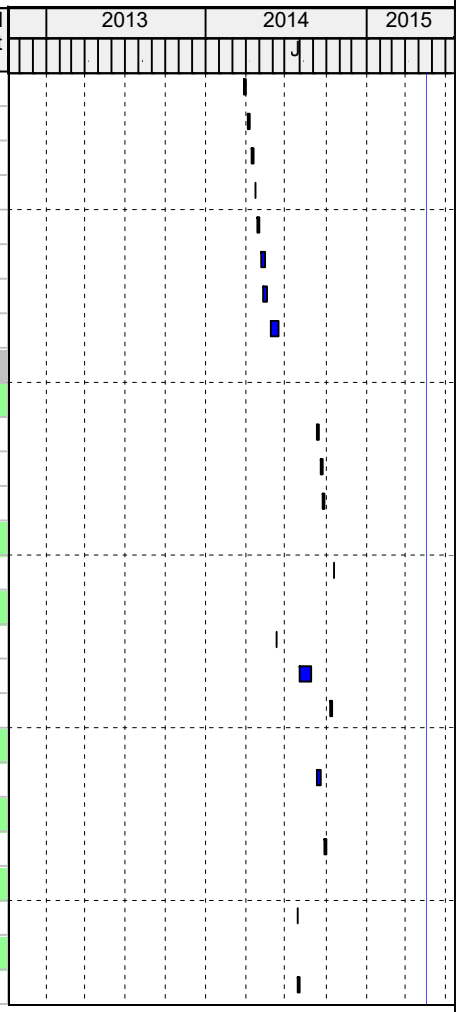



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |
| RF-4018 | TR - Terrace Roof - Green Roofing System | 5 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| RF-4020 | TR - Terrace Roof - Install sheet metal capping[DELE | 1 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4022 | TR - Terrace Roof - Install deocrative metal railing | 3 | 0 | 04-May-15 A | 05-May-15 A | |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Perimeter Framing / Sul | 10 | 0 | 02-Jun-14 A | 08-Jul-14 A | |
| RF-4002 | Tower Roof - Roofing System | 10 | 0 | 20-Aug-14 A | 17-Sep-14 A | |
| **PH - Roof - (elev 173')** | | | | | | |
| RF-4030 | PH - Roofing System | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| RF-4032 | PH - Coping / Flashing [DELETED] | 3 | 0 | 01-Sep-14 A | 01-Sep-14 A | |
| **Rough-In's** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6002 | LL4 - Layout | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| LL4-6008 | LL4 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL4-6012 | LL4 - Fire Sprinkler Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6014 | LL4 - Plumbing Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6018 | LL4 - HVAC Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6004 | LL4 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL4-6016 | LL4 - Electrical Rl | 10 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties Rl | 8 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6010 | LL4 - Elevator pits | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| LL4-6020 | LL4 - H Mtl Frames | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL4-6024 | LL4 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6002 | LL3 - Layout | 1 | 0 | 19-Nov-13 A | 19-Nov-13 A | |

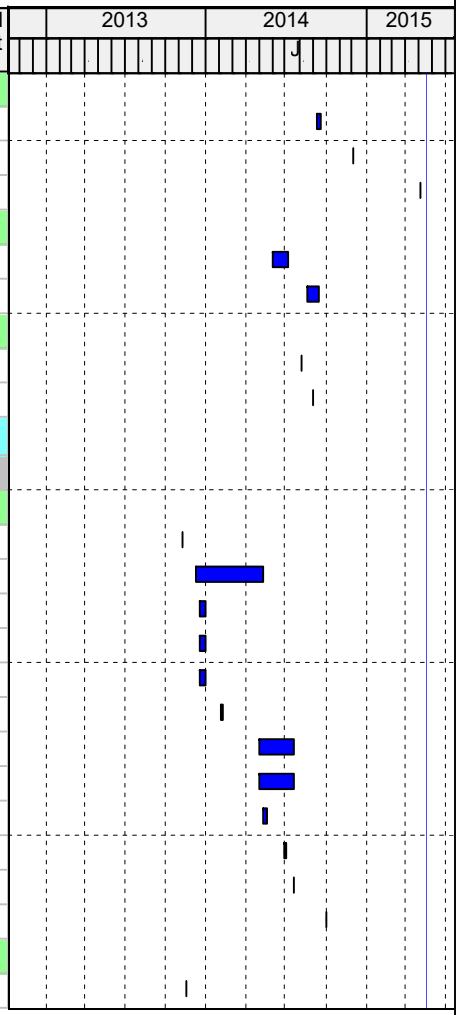


Actual Work | Critical Remai...
Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-6008 | LL3 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL3-6012 | LL3 - Fire Sprinkler RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6014 | LL3 - Plumbing RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6018 | LL3 - HVAC RI | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6004 | LL3 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL3-6020 | LL3 - H Mtl Frames | 3 | 0 | 08-May-14 A | 09-May-14 A | |
| LL3-6010 | LL3 - F/P Curbs | 5 | 0 | 19-May-14 A | 19-May-14 A | |
| LL3-6016 | LL3 - Electrical RI | 2 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties RI | 8 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL3-6024 | LL3 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6002 | LL2 - Layout | 1 | 0 | 14-Jan-14 A | 14-Jan-14 A | |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| LL2-6012 | LL2 - Fire Sprinkler RI | 10 | 0 | 21-Jan-14 A | 03-Feb-14 A | |
| LL2-6014 | LL2 - Plumbing RI | 10 | 0 | 21-Jan-14 A | 14-Feb-14 A | |
| LL2E-6016 | LL2 - Electrical RI | 8 | 0 | 03-Feb-14 A | 17-Mar-14 A | |
| LL2-6016 | LL2 - Electrical RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2-6018 | LL2 - HVAC RI | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2–6004 | LL2 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL2E-6004 | LL2 - CMU Walls | 10 | 0 | 04-Mar-14 A | 09-May-14 A | |
| LL2E-6012 | LL2 - Fire Sprinkler RI | 8 | 0 | 21-Mar-14 A | 01-Apr-14 A | |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 24-Apr-14 A | |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 3 | 0 | 23-Apr-14 A | 21-Jul-14 A | |
| LL2E-6020 | LL2 - H Mtl Frames | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| LL2-6020 | LL2 - H Mtl Frames | 3 | 0 | 12-May-14 A | 13-May-14 A | |
| LL2E-6008 | LL2 - Int Wall Framing | 5 | 0 | 13-May-14 A | 22-Jun-14 A | |

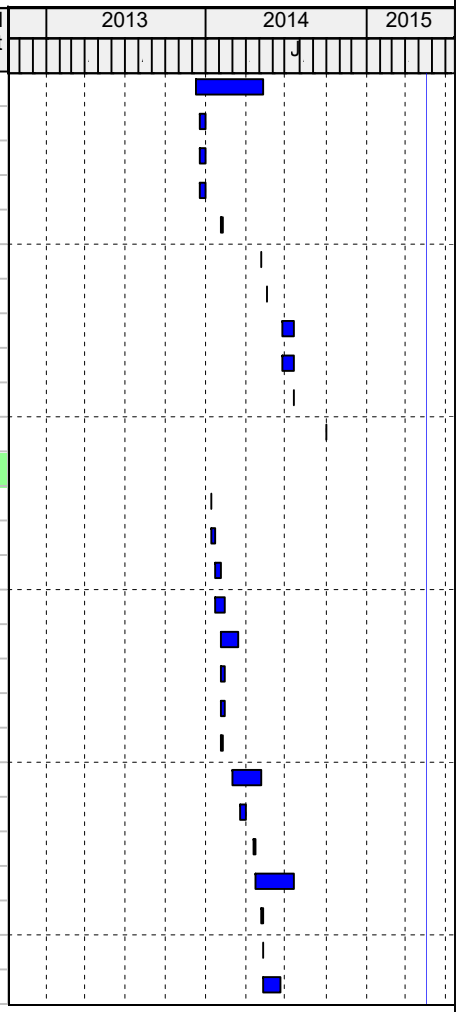



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2E-6014 | LL2 - Plumbing RI | 8 | 0 | 13-May-14 A | 30-May-14 A | |
| LL2E-6018 | LL2 - HVAC RI | 8 | 0 | 13-May-14 A | 04-Aug-14 A | |
| LL2E-6022 | LL2 - Fire Alarm / Elec Specialties RI (East of 10) | 8 | 0 | 13-May-14 A | 22-Sep-14 A | |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties RI (West of 10) | 8 | 0 | 19-May-14 A | 22-Sep-14 A | |
| LL2-6015 | LL2 - Main Elect Room Set Equip / RI - Power to Ma | 15 | 0 | 30-Jun-14 A | 26-Sep-14 A | |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 0 | 16-Jul-14 A | 21-Jul-14 A | |
| LL2-6024 | LL2 - Inspections | 2 | 0 | 15-Sep-14 A | 03-Oct-14 A | |
| LL2-6010 | F/P Curbs at Garage | 3 | 3 | 26-May-15 | 28-May-15 | 2 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6002 | Layout | 3 | 0 | 03-Jan-14 A | 08-Jan-14 A | |
| LL1-6008 | Int Wall Framing & Inspection | 6 | 0 | 08-Jan-14 A | 21-Jul-14 A | |
| LL1-Z2-6002 | Layout | 3 | 0 | 08-Jan-14 A | 14-Jan-14 A | |
| LL1-Z3-6002 | Layout | 3 | 0 | 14-Jan-14 A | 17-Jan-14 A | |
| LL1-Z2-6008 | Int Wall Framing & Inspection | 6 | 0 | 17-Jan-14 A | 01-Aug-14 A | |
| LL1-Z3-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-Jan-14 A | 04-Aug-14 A | |
| LL1-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 09-May-14 A | |
| LL1-Z2-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 28-Apr-14 A | |
| LL1-Z3-6004 | CMU Walls (At All Areas North of Q-Line) | 3 | 0 | 03-Feb-14 A | 13-May-14 A | |
| LL1C-6012 | Complete Fire Sprinkler RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6016 | Complete Electrical RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 10 | 0 | 17-Feb-14 A | 16-Sep-14 A | |
| LL1C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 30-Apr-14 A | |
| LL1-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |

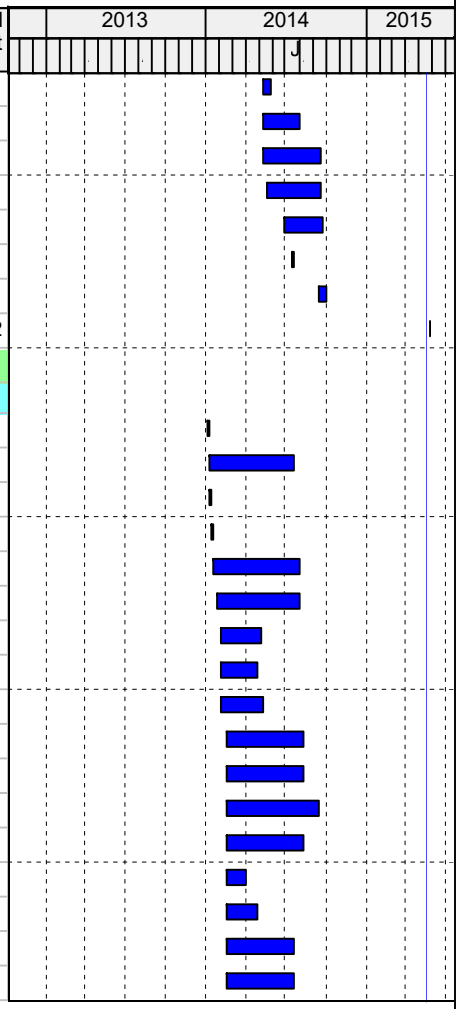


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-Z2-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z2-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z3-6012 | Fire Sprinkler RI (At All Areas North of Q-Line) | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z3-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 11-Sep-14 A | |
| LL1-Z3-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z2C-6012 | Complete Fire Sprinkler RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6014 | Complete Plumbing RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6016 | Complete Electrical RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 15 | 0 | 24-Feb-14 A | 15-Sep-14 A | |
| LL1-Z2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2-6020 | Hollow Metal Door Frames | 5 | 0 | 17-Mar-14 A | 04-Apr-14 A | |
| LL1-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| LL1-Z3-6020 | Hollow Metal Door Frames (At All Areas North of Q-Lir | 1 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| L1B-6004 | CMU Walls [including East Service Corridor] | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L1L-6002 | Layout [including back of house] | 3 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 29-Apr-14 A | |
| L1B-6008 | Int Wall Framing & Inspection | 6 | 0 | 21-Apr-14 A | 08-Aug-14 A | |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 5 | 0 | 25-Apr-14 A | 21-Jul-14 A | |
| LL1C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L1K-6004 | CMU Walls [including public restroom] | 3 | 0 | 05-May-14 A | 08-May-14 A | |
| L1K-6002 | Layout [including public restroom] | 3 | 0 | 08-May-14 A | 12-May-14 A | |

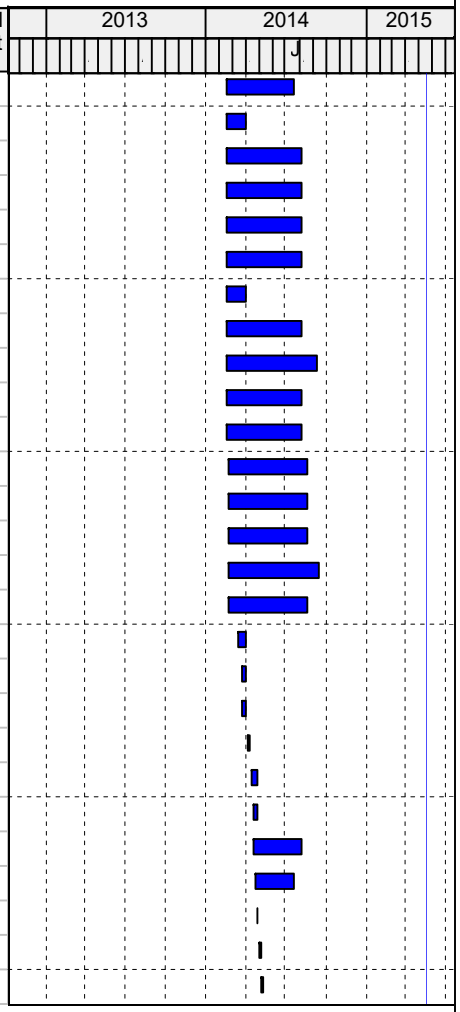



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-6008 | Int Wall Framing & Inspection | 4 | 0 | 09-May-14 A | 22-Aug-14 A | |
| L1B-6002 | Layout [including East Service Corridor] | 3 | 0 | 14-May-14 A | 27-May-14 A | |
| L1L-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-May-14 A | 06-Oct-14 A | |
| L1L-6004 | CMU Walls [including back of house] | 3 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L1K-6012 | Fire Sprinkler RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6014 | Plumbing RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6016 | Electrical RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1K-6018 | HVAC RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1B-6014 | Plumbing RI [including East Service Corridor] | 10 | 0 | 16-Jun-14 A | 24-Jun-14 A | |
| L1B-6018 | HVAC RI | 10 | 0 | 20-Jun-14 A | 15-Aug-14 A | |
| L1B-6012 | Fire Sprinkler RI | 10 | 0 | 21-Jun-14 A | 15-Aug-14 A | |
| L1L-6018 | HVAC RI | 5 | 0 | 23-Jun-14 A | 13-Oct-14 A | |
| L1L-6014 | Plumbing RI | 5 | 0 | 24-Jun-14 A | 28-Oct-14 A | |
| L1L-6010 | CMU Seismic Clips [including back of house] [DELET | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1L-6012 | Fire Sprinkler RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |
| L1L-6016 | Electrical RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |
| L1L-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 27-Jun-14 A | 13-Oct-14 A | |
| L1K-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 27-Jun-14 A | 29-Sep-14 A | |
| LL1-Z3-6009 | Frame Ceilings [DELETED] | 4 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1B-6016 | Electrical RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| L1B-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| LL1-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-Z2-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L1B-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-6024 | Inspections for Cover | 1 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L1B-6020 | Hollow Metal Door Frames | 5 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| LL1-Z3-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |

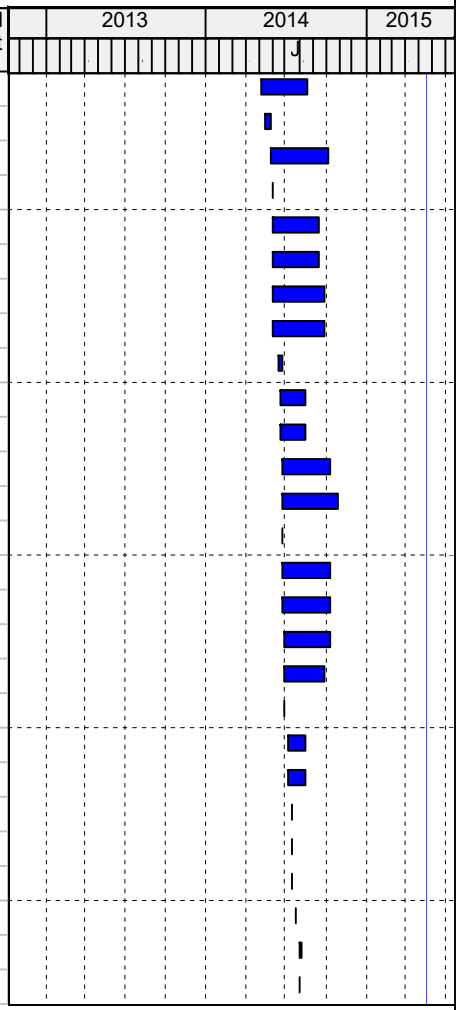



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 06-Aug-14 A | |
| LL1-Z2-6024 | Inspections for Cover | 2 | 0 | 07-Aug-14 A | 08-Aug-14 A | |
| L1K-6020 | Hollow Metal Door Frames | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-Z2-6009 | Frame Ceilings & Inspection | 6 | 0 | 22-Aug-14 A | 13-Oct-14 A | |
| L1L-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Aug-14 A | 13-Oct-14 A | |
| LL1-6009 | Frame Ceilings & Inspection (except for bar redesign | 9 | 0 | 02-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3-6024 | Inspections for Cover | 2 | 0 | 12-Sep-14 A | 12-Sep-14 A | |
| LL1-Z3C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6016 | Complete Electrical RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3C-6018 | Complete HVAC RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| L1KC-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 4 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L1B-6024 | Inspections for Cover (Main Ballroom N/S/W Walls & | 3 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1K-6024 | Inspections for Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1KC-6014 | Complete Plumbing RI @ Ceilings & Inspection | 4 | 0 | 02-Oct-14 A | 07-Oct-14 A | |
| L1BC-6014 | Complete Plumbing RI @ Ceilings | 7 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L1KC-6018 | Complete HVAC RI @ Ceilings & Inspection | 4 | 0 | 06-Oct-14 A | 10-Nov-14 A | |
| L1KC-6016 | Complete Electrical RI @ Ceilings & Inspection | 3 | 0 | 20-Oct-14 A | 10-Nov-14 A | |
| L1KC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 3 | 0 | 20-Oct-14 A | 10-Nov-14 A | |
| L1L-6024 | Inspections for Cover | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L1L-6009 | Frame ceilings & inspection at high ceiling | 13 | 0 | 24-Nov-14 A | 20-Jan-15 A | |
| L1B-6009 | Frame Ceilings & inspection at Main Ballroom (per re | 5 | 0 | 04-Dec-14 A | 16-Jan-15 A | |
| L1LC-6012 | Complete fire sprinkler RI @ ceilings | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1LC-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| L1LC-6016 | Complete electrical rough-in @ ceilings & inspection | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1LC-6018 | Complete HVAC RI @ Ceilings | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |

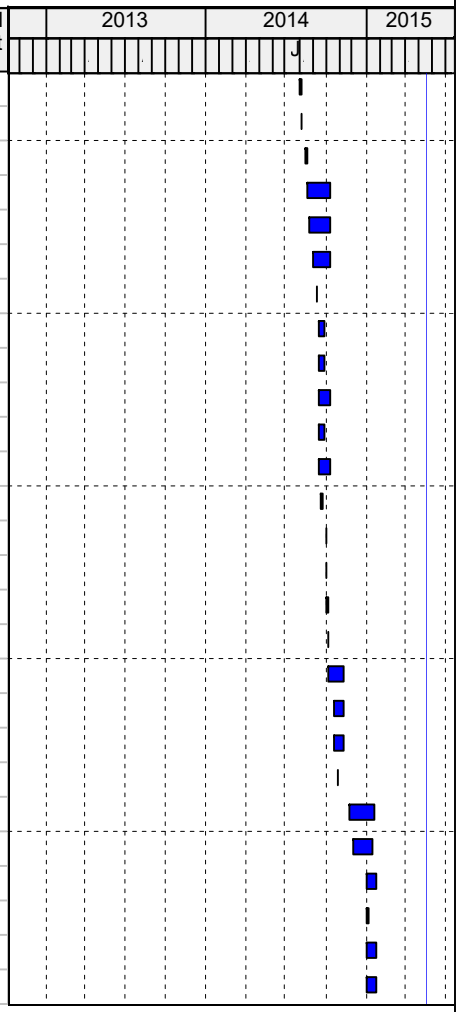


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1LC-6022 | Complete fire alarm/elec specialties Rl @ ceilings & ir | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1K-6009 | Frame ceilings & inspection at public restroom | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L1B-8118 | Lighting & electrical trim at Ballrooms | 7 | 0 | 07-Apr-15 A | 17-Apr-15 A | |
| L1B-8112 | Fire sprinkler trim at Ballrooms | 2 | 0 | 13-Apr-15 A | 14-Apr-15 A | |
| L1B-8204 | HVAC trim at Ballrooms | 5 | 0 | 13-Apr-15 A | 15-Apr-15 A | |
| L1BC-6022 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 13-Apr-15 A | 14-Apr-15 A | |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 0 | 17-Apr-14 A | 09-May-14 A | |
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6006 | L2 - Support Frame/Sheathing for Metal Panels | 6 | 0 | 23-Apr-14 A | 07-Aug-14 A | |
| L02-6008 | L2 - Int Wall Framing | 10 | 0 | 25-Apr-14 A | 17-Jul-14 A | |
| L02-6014 | L2 - Plumbing Rl | 15 | 0 | 28-Apr-14 A | 07-Aug-14 A | |
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 0 | 28-Apr-14 A | 09-May-14 A | |
| L02-6004 | L2 - CMU Walls | 5 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L02-6002 | L2 - Layout | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L02-6018 | L2 - HVAC Rl (including equipment) | 20 | 0 | 18-Jun-14 A | 10-Sep-14 A | |
| L02-6016 | L2 - Electrical Rl | 10 | 0 | 24-Jun-14 A | 14-Aug-14 A | |
| L02-6022 | L2 - Fire Alarm / Elec Specialties Rl | 10 | 0 | 24-Jun-14 A | 10-Oct-14 A | |
| L02-6012 | L2 - Fire Sprinkler Rl | 10 | 0 | 26-Jun-14 A | 07-Aug-14 A | |
| L02-6020 | L2 - H Mtl Frames | 5 | 0 | 11-Jul-14 A | 17-Jul-14 A | |
| L02-6024 | L2 - Inspections - North Half | 2 | 0 | 10-Oct-14 A | 20-Oct-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L04-6012 | Fire Sprinkler Mains | 5 | 0 | 01-Feb-14 A | 03-Apr-14 A | |
| L03-8219 | HVAC Risers | 5 | 0 | 11-Feb-14 A | 23-Mar-14 A | |
| L03-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 11-Feb-14 A | 03-Mar-14 A | |

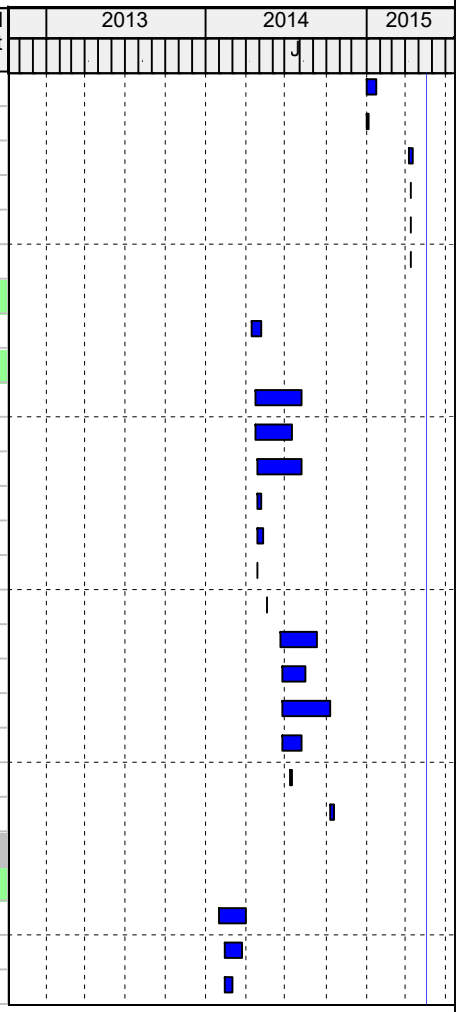



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6002 | Layout | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| L04-8219 | HVAC Risers | 5 | 0 | 13-Feb-14 A | 23-Mar-14 A | |
| L05-8219 | HVAC Risers | 5 | 0 | 17-Feb-14 A | 03-Mar-14 A | |
| L03-6008 | Frame Shaft Walls | 3 | 0 | 18-Feb-14 A | 26-Mar-14 A | |
| L04-6002 | Layout | 5 | 0 | 19-Feb-14 A | 25-Feb-14 A | |
| L04-6008 | Frame Shaft Walls | 3 | 0 | 20-Feb-14 A | 26-Mar-14 A | |
| L03-6011 | PreRock Shafts | 2 | 0 | 24-Feb-14 A | 25-Mar-14 A | |
| L03-6010 | Frame Walls | 5 | 0 | 25-Feb-14 A | 25-Mar-14 A | |
| L05-6002 | Layout | 5 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| L04-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 28-Feb-14 A | 05-Mar-14 A | |
| L03-6016 | Electrical RI | 5 | 0 | 03-Mar-14 A | 04-Apr-14 A | |
| L03-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 12-Mar-14 A | |
| L04-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 13-Mar-14 A | |
| L04-6010 | Frame Walls | 5 | 0 | 04-Mar-14 A | 05-Jun-14 A | |
| L05-6008 | Frame Shaft Walls | 3 | 0 | 05-Mar-14 A | 27-Mar-14 A | |
| L06-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L07-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L05-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 06-Mar-14 A | 21-Mar-14 A | |
| L03-6020 | Install Hollow Metal Frames | 3 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L04-6020 | Install Hollow Metal Frames | 3 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L05-6010 | Frame Walls | 5 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L06-6002 | Layout | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L04-6011 | PreRock Shafts | 2 | 0 | 18-Mar-14 A | 25-Mar-14 A | |
| L05-6009 | Inspect Shafts | 1 | 0 | 18-Mar-14 A | 18-Mar-14 A | |
| L05-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| L06-6008 | Frame Shaft Walls | 3 | 0 | 19-Mar-14 A | 03-Apr-14 A | |
| L06-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 27-Mar-14 A | |

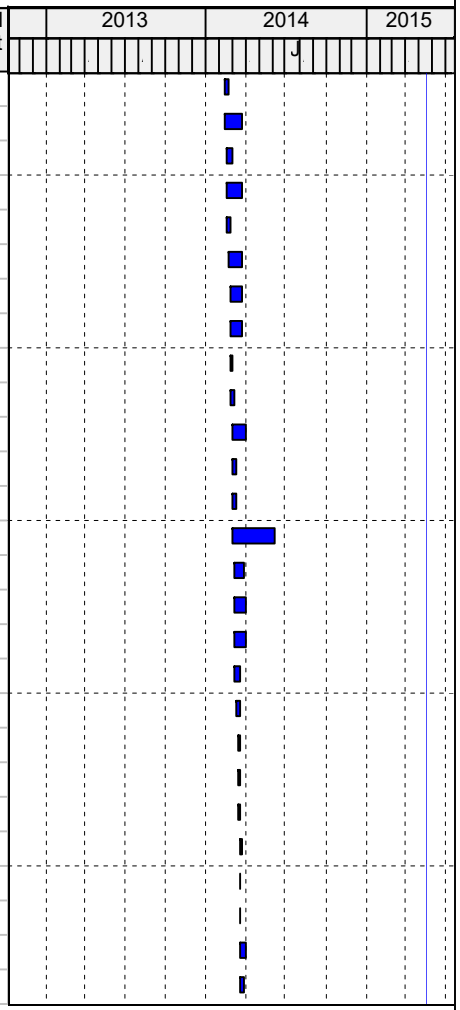


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6016 | Electrical RI | 5 | 0 | 20-Mar-14 A | 09-Apr-14 A | |
| L05-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 26-Mar-14 A | |
| L06-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 07-Apr-14 A | |
| L07-6002 | Layout | 5 | 0 | 24-Mar-14 A | 30-Apr-14 A | |
| L03-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L03-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L05-6016 | Electrical RI | 5 | 0 | 25-Mar-14 A | 05-Jun-14 A | |
| L04-6019 | Complete Top Out GWB | 2 | 0 | 26-Mar-14 A | 06-Jun-14 A | |
| L05-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L06-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| L03-6019 | Complete Top Out GWB | 2 | 0 | 27-Mar-14 A | 02-May-14 A | |
| L08-6002 | Layout | 5 | 0 | 27-Mar-14 A | 02-Apr-14 A | |
| L05-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 28-Mar-14 A | 03-Apr-14 A | |
| L06-6010 | Frame Walls | 5 | 0 | 28-Mar-14 A | 07-Apr-14 A | |
| L03-6012 | Fire Sprinkler Mains | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L07-6008 | Frame Shaft Walls | 3 | 0 | 31-Mar-14 A | 03-Apr-14 A | |
| L05-6019 | Complete Top Out GWB | 2 | 0 | 01-Apr-14 A | 08-Apr-14 A | |
| L07-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 01-Apr-14 A | 11-Apr-14 A | |
| L08-6008 | Frame Shaft Walls | 3 | 0 | 02-Apr-14 A | 21-Apr-14 A | |
| L03-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L04-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L05-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L06-6016 | Electrical RI | 5 | 0 | 03-Apr-14 A | 15-Apr-14 A | |
| L07-6009 | Inspect Shafts | 1 | 0 | 03-Apr-14 A | 03-Apr-14 A | |
| L07-6011 | PreRock Shafts | 2 | 0 | 03-Apr-14 A | 07-Apr-14 A | |

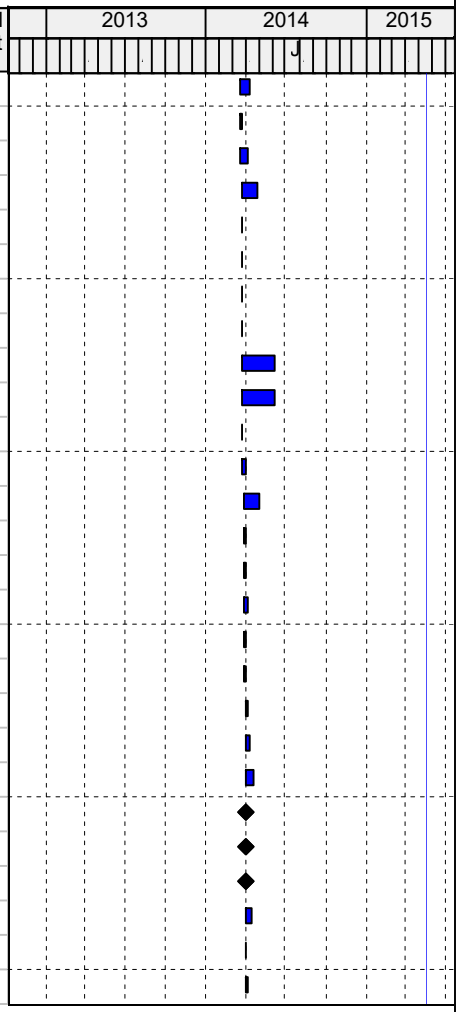


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6012 | Fire Sprinkler Mains | 5 | 0 | 04-Apr-14 A | 30-Apr-14 A | |
| L06-6012 | Fire Sprinkler Mains | 5 | 0 | 07-Apr-14 A | 30-Apr-14 A | |
| L06-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L06-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L07-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| L07-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L03-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L03-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L04-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L06-6009 | Inspect Shafts | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L06-6019 | Complete Top Out GWB | 2 | 0 | 08-Apr-14 A | 18-Apr-14 A | |
| L07-6010 | Frame Walls | 5 | 0 | 08-Apr-14 A | 15-Apr-14 A | |
| L08-6011 | PreRock Shafts | 2 | 0 | 08-Apr-14 A | 23-Apr-14 A | |
| L09-6002 | Layout | 5 | 0 | 08-Apr-14 A | 26-Apr-14 A | |
| L03-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 09-Apr-14 A | 08-May-14 A | |
| L03-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L05-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 09-Apr-14 A | 14-Apr-14 A | |
| L08-6009 | Inspect Shafts | 1 | 0 | 09-Apr-14 A | 25-Apr-14 A | |
| L09-6008 | Frame Shaft Walls | 3 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| L08-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| L04-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 15-Apr-14 A | 16-Apr-14 A | |
| L07-6012 | Fire Sprinkler Mains | 5 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| L07-6016 | Electrical RI | 5 | 0 | 15-Apr-14 A | 12-May-14 A | |
| L07-6020 | Install Hollow Metal Frames | 3 | 0 | 16-Apr-14 A | 23-Apr-14 A | |
| L05-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 17-Apr-14 A | 25-Apr-14 A | |
| L06-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 17-Apr-14 A | 12-May-14 A | |
| L06-6023 | Inspection of Exterior Framing | 0 | 0 | 17-Apr-14 A | | |

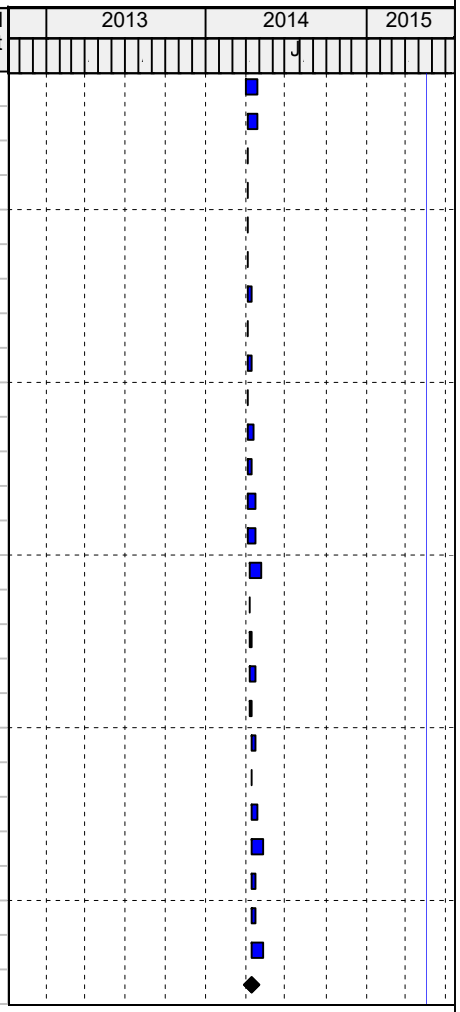



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8219 | HVAC Risers | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L09-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L04-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 18-Apr-14 A | 20-Apr-14 A | |
| L04-6028 | PreRock at Heat Pumps | 2 | 0 | 20-Apr-14 A | 22-Apr-14 A | |
| L08-8219 | HVAC Risers | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6009 | Inspect Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6011 | PreRock Shafts | 2 | 0 | 22-Apr-14 A | 24-Apr-14 A | |
| L04-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L06-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 23-Apr-14 A | 25-Apr-14 A | |
| L08-6020 | Install Hollow Metal Frames | 3 | 0 | 23-Apr-14 A | 13-May-14 A | |
| L11-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L11-8220 | Plumbing Risers - Install | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L04-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L09-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L10-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L10-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 20-May-14 A | |
| L12-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L04-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 25-Apr-14 A | 11-Jun-14 A | |
| L04-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L09-6010 | Frame Walls | 5 | 0 | 25-Apr-14 A | 20-May-14 A | |
| L09-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L10-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L11-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 30-Apr-14 A | |
| L12-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L08-6010 | Frame Walls | 5 | 0 | 26-Apr-14 A | 30-Apr-14 A | |

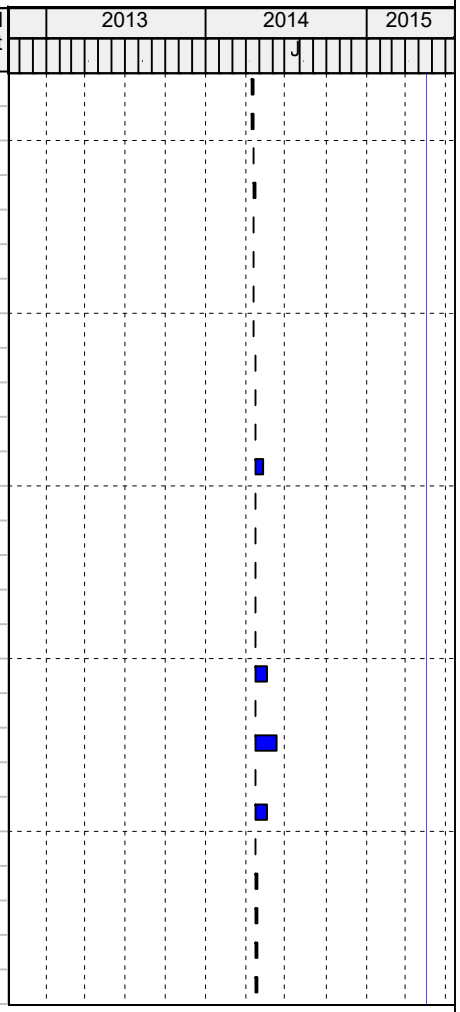



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-6002 | Layout | 5 | 0 | 27-Apr-14 A | 27-Apr-14 A | |
| L04-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 28-Apr-14 A | 30-Apr-14 A | |
| L05-6018 | HVAC RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6028 | PreRock at Heat Pumps | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L07-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 28-Apr-14 A | 12-May-14 A | |
| L10-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-Apr-14 A | 22-May-14 A | |
| L11-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L12-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L05-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| L05-6028 | PreRock at Heat Pumps | 2 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L06-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 09-May-14 A | |
| L06-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L06-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L08-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L08-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L09-6020 | Install Hollow Metal Frames | 3 | 0 | 29-Apr-14 A | 20-May-14 A | |
| L09-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L10-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L04-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 30-Apr-14 A | 02-May-14 A | |

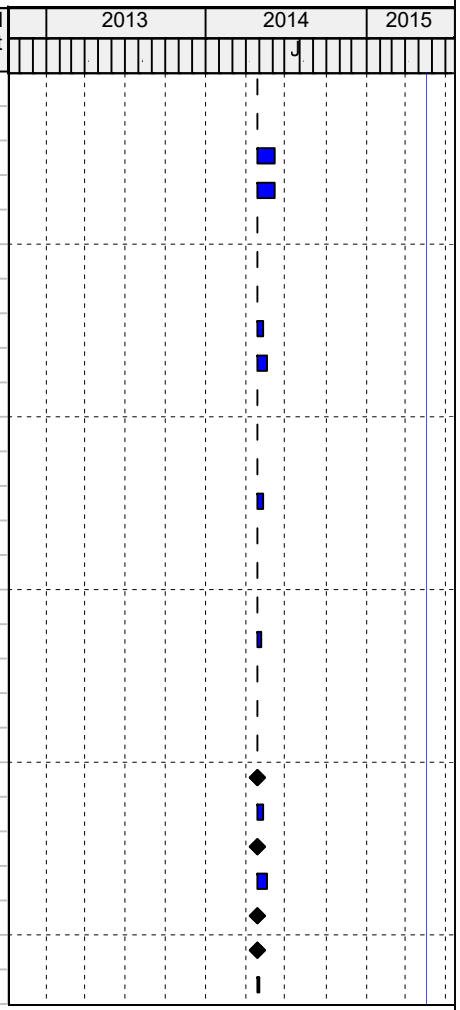



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6019 | Complete Top Out GWB | 2 | 0 | 30-Apr-14 A | 06-Jun-14 A | |
| L11-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L12-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L03-6028 | PreRock at Heat Pumps | 2 | 0 | 01-May-14 A | 02-May-14 A | |
| L05-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L06-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L03-6014 | Set Tubs & Plumbing RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L05-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L05-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| L06-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L06-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 09-May-14 A | |
| L03-6018 | HVAC RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L03-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 06-May-14 A | 06-May-14 A | |
| L07-6014 | Set Tubs & Plumbing RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L07-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 06-May-14 A | 09-May-14 A | |
| L03-6004 | CMU Wall/Clips | 3 | 0 | 07-May-14 A | 08-May-14 A | |
| L03-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L03-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 08-May-14 A | 13-May-14 A | |
| L03-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6004 | CMU Walls | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6018 | HVAC RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L11-6010 | Frame Walls | 5 | 0 | 09-May-14 A | 15-May-14 A | |

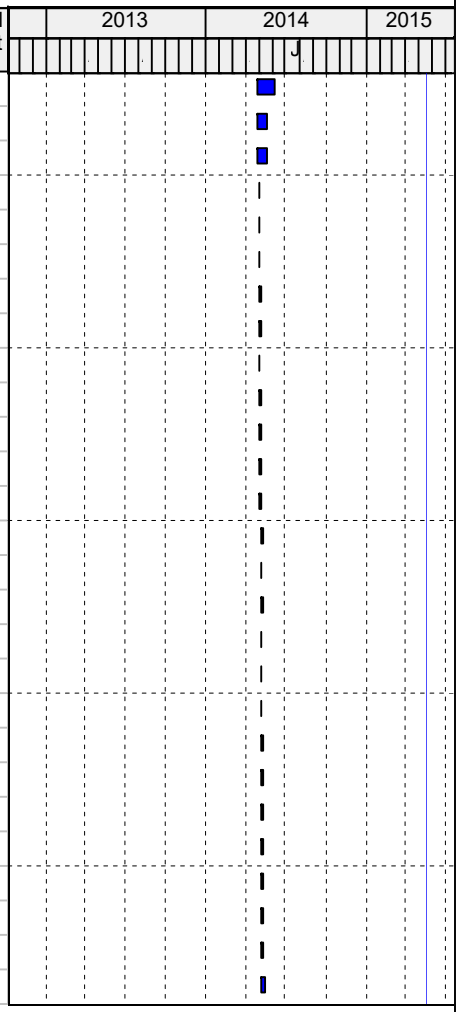



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 12-May-14 A | 05-Jun-14 A | |
| L07-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 12-May-14 A | 13-May-14 A | |
| L11-6020 | Install Hollow Metal Frames | 3 | 0 | 12-May-14 A | 14-May-14 A | |
| L11-6019 | Complete Top Out GWB | 2 | 0 | 12-May-14 A | 14-May-14 A | |
| L14-6002 | Layout | 5 | 0 | 12-May-14 A | 14-May-14 A | |
| L15-6002 | Layout | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L05-6004 | CMU Walls | 3 | 0 | 13-May-14 A | 13-May-14 A | |
| L06-6018 | HVAC Rl | 5 | 0 | 13-May-14 A | 25-Jun-14 A | |
| L06-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 13-May-14 A | 14-Jul-14 A | |
| L07-6018 | HVAC Rl | 5 | 0 | 13-May-14 A | 05-Jun-14 A | |
| L07-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| L07-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 13-May-14 A | 13-May-14 A | |
| L14-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L16-6002 | Layout | 5 | 0 | 13-May-14 A | 16-May-14 A | |
| L06-6004 | CMU Walls | 3 | 0 | 14-May-14 A | 14-May-14 A | |
| L07-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 15-May-14 A | |
| L08-6012 | Fire Sprinkler Mains | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6002 | Layout | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L07-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 16-May-14 A | 25-Jun-14 A | |
| L08-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L11-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L12-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |

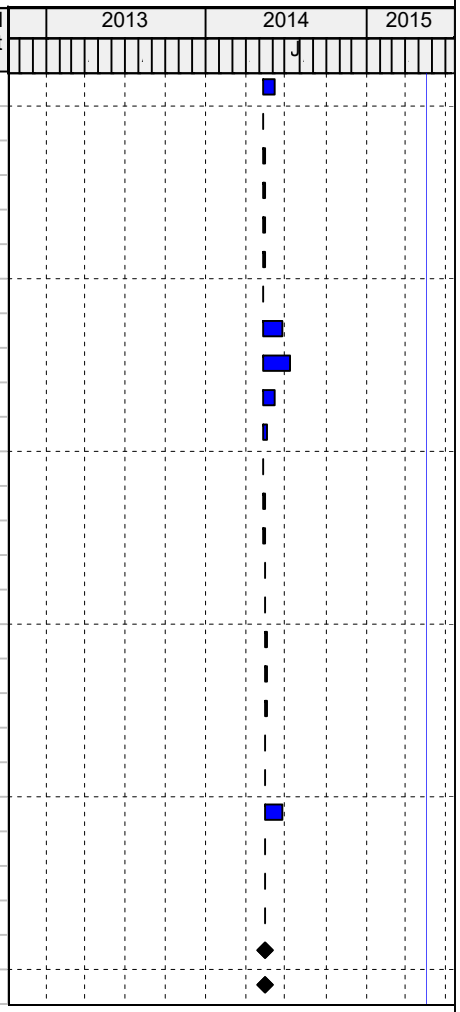



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L08-6028 | PreRock at Heat Pumps | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L09-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L10-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L11-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L15-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 19-May-14 A | 19-May-14 A | |
| L07-6028 | PreRock at Heat Pumps | 2 | 0 | 20-May-14 A | 21-May-14 A | |
| L07-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L08-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 20-May-14 A | 21-May-14 A | |
| L10-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L11-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L14-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L07-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 21-May-14 A | 27-May-14 A | |
| L08-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L08-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L09-6028 | PreRock at Heat Pumps | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L10-6014 | Set Tubs & Plumbing RI | 5 | 0 | 21-May-14 A | 27-Jun-14 A | |
| L10-6010 | Frame Walls | 5 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6019 | Complete Top Out GWB | 2 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L11-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L12-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L14-8220 | Plumbing Risers - Install | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L15-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L16-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |

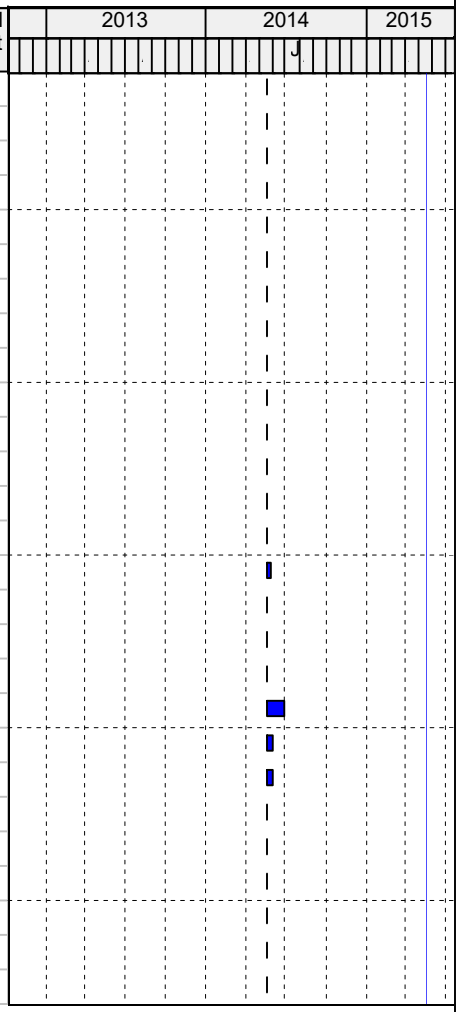



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| L08-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 22-May-14 A | 22-May-14 A | |
| L10-6012 | Fire Sprinkler Mains | 5 | 0 | 22-May-14 A | 27-May-14 A | |
| L08-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L09-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6020 | Install Hollow Metal Frames | 3 | 0 | 23-May-14 A | 03-Jun-14 A | |
| L10-6028 | PreRock at Heat Pumps | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L14-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L15-8220 | Plumbing Risers - Install | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L09-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 27-May-14 A | 27-May-14 A | |
| L12-6010 | Frame Walls | 5 | 0 | 27-May-14 A | 02-Jun-14 A | |
| L08-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L09-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 28-May-14 A | 28-May-14 A | |
| L10-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 28-May-14 A | 03-Jun-14 A | |
| L14-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L15-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-May-14 A | 30-May-14 A | |
| L16-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 28-May-14 A | 28-May-14 A | |
| L16-8220 | Plumbing Risers - Install | 2 | 0 | 28-May-14 A | 29-May-14 A | |
| L08-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 29-May-14 A | 30-May-14 A | |
| L10-6016 | Electrical RI | 5 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L10-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| L12-6012 | Fire Sprinkler Mains | 5 | 0 | 30-May-14 A | 26-Jun-14 A | |
| L12-6020 | Install Hollow Metal Frames | 3 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L15-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L17-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |

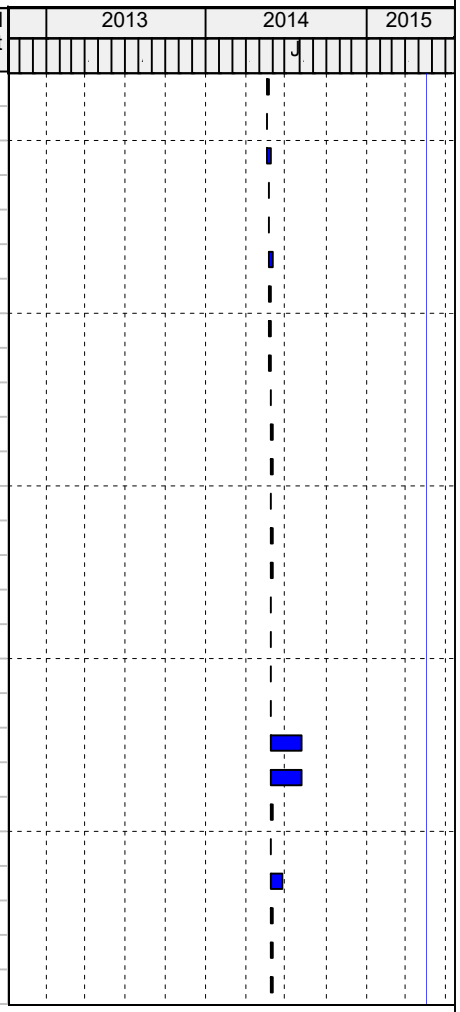



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8220 | Plumbing Risers - Install | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L10-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L11-6016 | Electrical RI | 5 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L11-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L12-6019 | Complete Top Out GWB | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L14-6020 | Install Hollow Metal Frames | 3 | 0 | 02-Jun-14 A | 05-Jun-14 A | |
| L14-6010 | Frame Walls | 5 | 0 | 02-Jun-14 A | 04-Jun-14 A | |
| L16-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| L14-6019 | Complete Top Out GWB | 2 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L16-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L10-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| L17-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 04-Jun-14 A | 11-Jun-14 A | |
| L08-6016 | Electrical RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L08-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L09-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L12-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L15-6010 | Frame Walls | 3 | 0 | 05-Jun-14 A | 11-Jun-14 A | |
| L09-6012 | Fire Sprinkler Mains | 5 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L09-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L11-6012 | Fire Sprinkler Mains | 4 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L12-6014 | Set Tubs & Plumbing RI | 4 | 0 | 06-Jun-14 A | 27-Jun-14 A | |
| L11-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jun-14 A | 11-Jun-14 A | |
| L09-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-Jun-14 A | 25-Jun-14 A | |
| L14-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L15-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L16-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L09-6016 | Electrical RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |

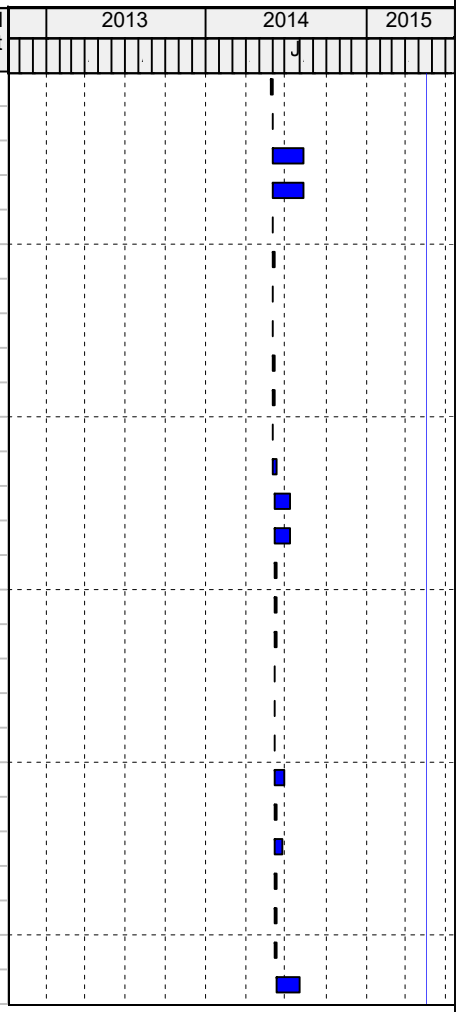



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L14-6014 | Set Tubs & Plumbing Rl | 4 | 0 | 10-Jun-14 A | 21-Jul-14 A | |
| L15-6020 | Install Hollow Metal Frames | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L15-6019 | Complete Top Out GWB | 2 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6014 | Set Tubs & Plumbing Rl | 4 | 0 | 11-Jun-14 A | 26-Jun-14 A | |
| L11-6028 | PreRock at Heat Pumps | 2 | 0 | 13-Jun-14 A | 14-Jun-14 A | |
| L11-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 14-Jun-14 A | 14-Jun-14 A | |
| L14-6012 | Fire Sprinkler Mains | 2 | 0 | 16-Jun-14 A | 27-Jun-14 A | |
| L14-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 18-Jun-14 A | 18-Jun-14 A | |
| L15-6023 | Inspection of Exterior Framing | 0 | 0 | 18-Jun-14 A | | |
| L17-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 18-Jun-14 A | 23-Jun-14 A | |
| L17-6010 | Frame Walls | 5 | 0 | 18-Jun-14 A | 29-Jul-14 A | |
| L10-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L12-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6023 | Inspection of Exterior Framing | 0 | 0 | 20-Jun-14 A | | |
| L15-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-Jun-14 A | 20-Jun-14 A | |
| L10-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-Jun-14 A | 23-Jun-14 A | |
| L15-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 22-Jun-14 A | 24-Jul-14 A | |
| L08-6018 | HVAC Rl | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L12-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L14-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L15-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |

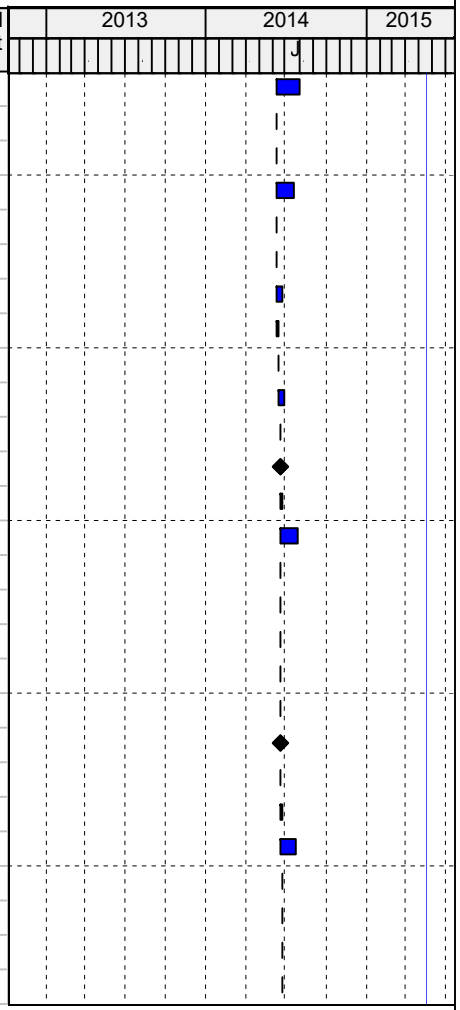



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-6221 | Frame Unit Ceilings | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| L11-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 24-Jun-14 A | 27-Jun-14 A | |
| L12-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L14-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6023 | Inspection of Exterior Framing | 0 | 0 | 24-Jun-14 A | | |
| L12-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| L12-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L14-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L15-6012 | Fire Sprinkler Mains | 2 | 0 | 25-Jun-14 A | 22-Jul-14 A | |
| L16-6023 | Inspection of Exterior Framing | 0 | 0 | 25-Jun-14 A | | |
| L03-6024 | Inspections for GWB Cover | 1 | 0 | 27-Jun-14 A | 27-Jun-14 A | |
| L09-6018 | HVAC RI | 3 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L09-6221 | Frame Unit Ceilings | 2 | 0 | 27-Jun-14 A | 30-Jun-14 A | |
| L12-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L14-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L15-6028 | PreRock at Heat Pumps | 2 | 0 | 30-Jun-14 A | 01-Jul-14 A | |
| L16-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 30-Jun-14 A | 30-Jun-14 A | |
| L16-6010 | Frame Walls | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| L16-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L15-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L15-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L04-6024 | Inspections for GWB Cover | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L10-6018 | HVAC RI | 3 | 0 | 07-Jul-14 A | 21-Jul-14 A | |
| L11-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L15-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L16-6012 | Fire Sprinkler Mains | 2 | 0 | 07-Jul-14 A | 24-Jul-14 A | |
| L16-6020 | Install Hollow Metal Frames | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |

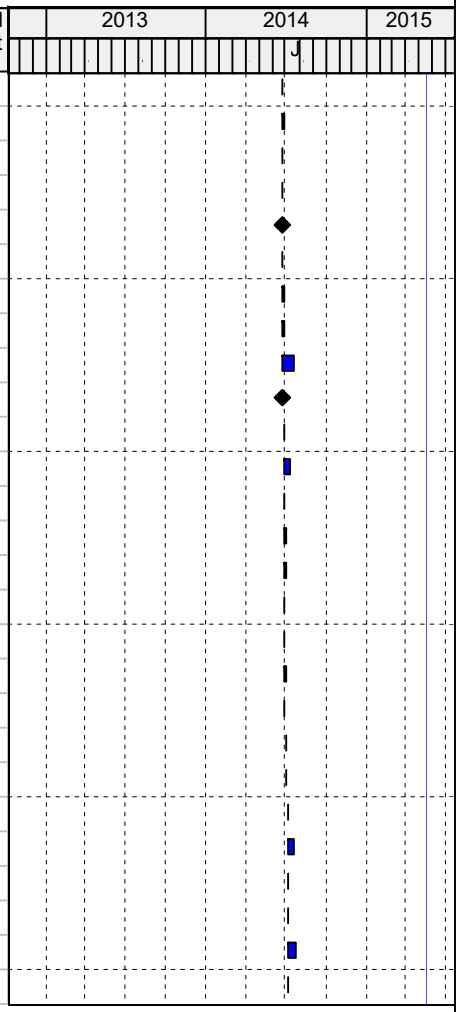



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-6028 | PreRock at Heat Pumps | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L17-6019 | Complete Top Out GWB | 1 | 0 | 07-Jul-14 A | 08-Aug-14 A | |
| L11-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L15-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 08-Jul-14 A | 04-Aug-14 A | |
| L17-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jul-14 A | 01-Aug-14 A | |
| L10-6221 | Frame Unit Ceilings | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| L17-6012 | Fire Sprinkler Mains | 2 | 0 | 09-Jul-14 A | 12-Aug-14 A | |
| L05-6024 | Inspections for GWB Cover | 2 | 0 | 10-Jul-14 A | 10-Jul-14 A | |
| L04-6000 | Tape/Finish GWB | 6 | 0 | 11-Jul-14 A | 23-Jul-14 A | |
| L16-6019 | Complete Top Out GWB | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L16-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L15-6018 | HVAC RI | 3 | 0 | 16-Jul-14 A | 18-Jul-14 A | |
| L16-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-6024 | Inspections for GWB Cover | 2 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6018 | HVAC RI | 3 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L16-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 21-Jul-14 A | 18-Aug-14 A | |
| L15-6013 | Fire Sprinkler Branch Lines | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| L03-6000 | Tape/Finish GWB | 6 | 0 | 23-Jul-14 A | 29-Jul-14 A | |
| L11-6018 | HVAC RI | 3 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L15-6221 | Frame Unit Ceilings | 2 | 0 | 23-Jul-14 A | 01-Aug-14 A | |
| L16-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L17-6020 | Install Hollow Metal Frames | 3 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| L11-6221 | Frame Unit Ceilings | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L12-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |

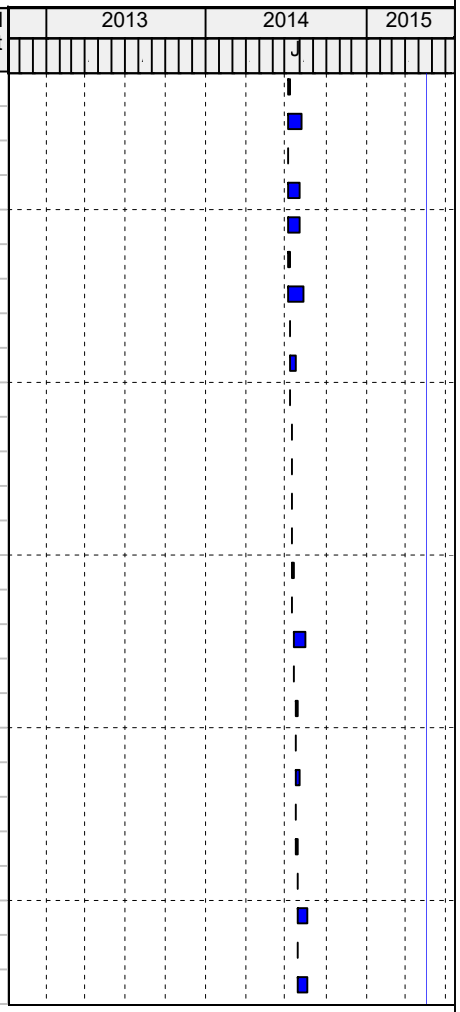



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L14-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L16-6014 | Set Tubs & Plumbing RI | 5 | 0 | 28-Jul-14 A | 18-Aug-14 A | |
| L07-6024 | Inspections for GWB Cover | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L12-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L05-6000 | Tape/Finish GWB | 6 | 0 | 31-Jul-14 A | 05-Aug-14 A | |
| L08-6024 | Inspections for GWB Cover | 2 | 0 | 31-Jul-14 A | 31-Jul-14 A | |
| L12-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L14-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L06-6000 | Tape/Finish GWB | 4 | 0 | 06-Aug-14 A | 11-Aug-14 A | |
| L09-6024 | Inspections for GWB Cover | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L07-6000 | Tape/Finish GWB | 5 | 0 | 07-Aug-14 A | 16-Aug-14 A | |
| L11-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 08-Aug-14 A | 14-Aug-14 A | |
| L17-6014 | Set Tubs & Plumbing RI | 5 | 0 | 08-Aug-14 A | 16-Sep-14 A | |
| L10-6024 | Inspections for GWB Cover | 2 | 0 | 11-Aug-14 A | 12-Aug-14 A | |
| L09-6000 | Tape/Finish GWB | 5 | 0 | 14-Aug-14 A | 19-Aug-14 A | |
| L08-6000 | Tape/Finish GWB | 5 | 0 | 16-Aug-14 A | 21-Aug-14 A | |
| L11-6024 | Inspections for GWB Cover | 2 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L16-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 18-Aug-14 A | 29-Aug-14 A | |
| L10-6000 | Tape/Finish GWB | 5 | 0 | 19-Aug-14 A | 23-Aug-14 A | |
| L16-6221 | Frame Unit Ceilings | 4 | 0 | 21-Aug-14 A | 26-Aug-14 A | |
| L17-6018 | HVAC RI | 3 | 0 | 21-Aug-14 A | 10-Sep-14 A | |
| L12-6024 | Inspections for GWB Cover | 2 | 0 | 22-Aug-14 A | 22-Aug-14 A | |

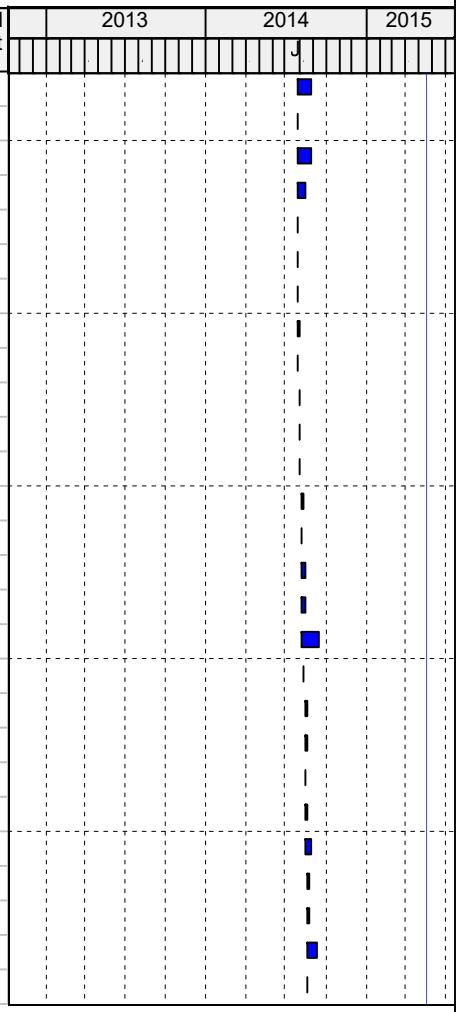



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6016 | Electrical RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L15-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L11-6000 | Tape/Finish GWB | 5 | 0 | 23-Aug-14 A | 29-Aug-14 A | |
| L17-6221 | Frame Unit Ceilings | 4 | 0 | 26-Aug-14 A | 28-Aug-14 A | |
| L14-6024 | Inspections for GWB Cover | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L16-6016 | Electrical RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L16-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L12-6000 | Tape/Finish GWB | 5 | 0 | 02-Sep-14 A | 08-Sep-14 A | |
| L15-6024 | Inspections for GWB Cover | 2 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L14-6000 | Tape/Finish GWB | 5 | 0 | 06-Sep-14 A | 11-Sep-14 A | |
| L15-6000 | Tape/Finish GWB | 4 | 0 | 12-Sep-14 A | 20-Sep-14 A | |
| L17-6016 | Electrical RI | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-6028 | PreRock at Heat Pumps | 2 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L17-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L17-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L17-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 24-Sep-14 A | 27-Sep-14 A | |
| L17-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L16-6024 | Inspections for GWB Cover | 1 | 0 | 08-Oct-14 A | 09-Oct-14 A | |
| L16-6000 | Tape/Finish GWB | 4 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6024 | Inspections for GWB Cover | 1 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6000 | Tape/Finish GWB | 6 | 0 | 30-Oct-14 A | 07-Nov-14 A | |
| **Mechanical Penthouse** | | | | | | |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 0 | 11-Jun-14 A | 20-Jun-14 A | |

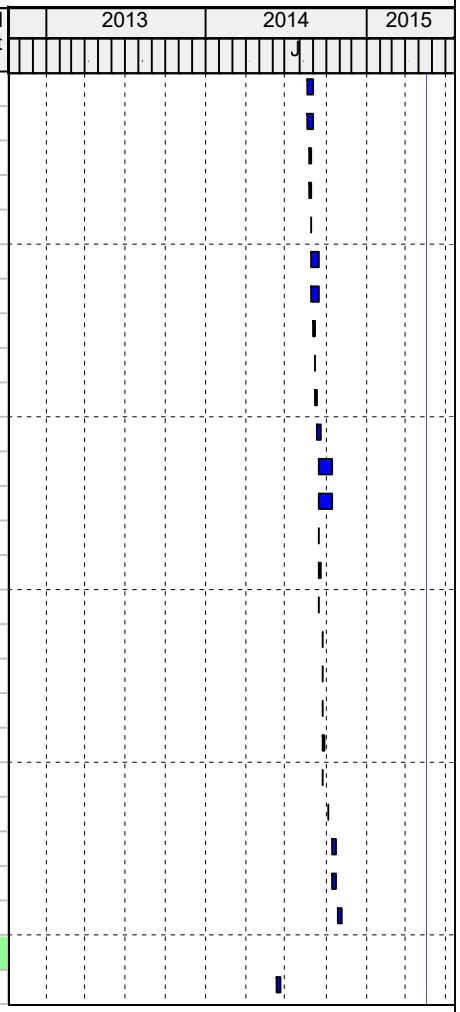



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-6006 | PH - Exterior Wall Framing (including PH roof parapet | 6 | 0 | 12-Jun-14 A | 14-Jul-14 A | |
| PH-6014 | PH - Plumbing/Piping RI | 40 | 0 | 25-Jun-14 A | 05-Nov-14 A | |
| PH-6002 | PH - Layout | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| PH-6008 | PH - Interior Wall Framing | 3 | 0 | 24-Jul-14 A | 08-Aug-14 A | |
| PH-6020 | PH - H Mtl Frames | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| PH-6012 | PH - Fire Sprinkler RI | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |
| PH-6018 | PH - HVAC RI | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |
| PH-6016 | PH - Electrical RI | 10 | 0 | 23-Sep-14 A | 14-Nov-14 A | |
| PH-6022 | PH - Fire Alarm / Elec Specialties RI | 10 | 0 | 23-Sep-14 A | 14-Nov-14 A | |
| **Finishes** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL4-8100 | LL4 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| LL4-8102 | LL4 - GWB Hang (incl. screw inspection) | 3 | 0 | 27-Oct-14 A | 10-Dec-14 A | |
| LL4-8114 | LL4 - Striping / Signage (DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL4-8104 | LL4 - Int Painting | 3 | 0 | 22-Dec-14 A | 24-Dec-14 A | |
| LL4-8122 | LL4 - Plumbing Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL4-8108 | Electrical trim & finish | 5 | 0 | 29-Dec-14 A | 16-Feb-15 A | |
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL4-8126 | Install doors & hardware | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL4-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 22-Jan-15 A | 26-Jan-15 A | |
| LL4-8124 | Flooring - VCT | 4 | 0 | 05-Feb-15 A | 06-Feb-15 A | |
| LL4-8110 | HVAC trim | 2 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| LL4-8134 | Final Cleaning | 2 | 2 | 26-May-15 | 27-May-15 | 7 |
| LL4-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 28-May-15 | 01-Jun-15 | 7 |
| LL4-8214 | LL4 Floor Complete | 0 | 0 | | 01-Jun-15 | 7 |

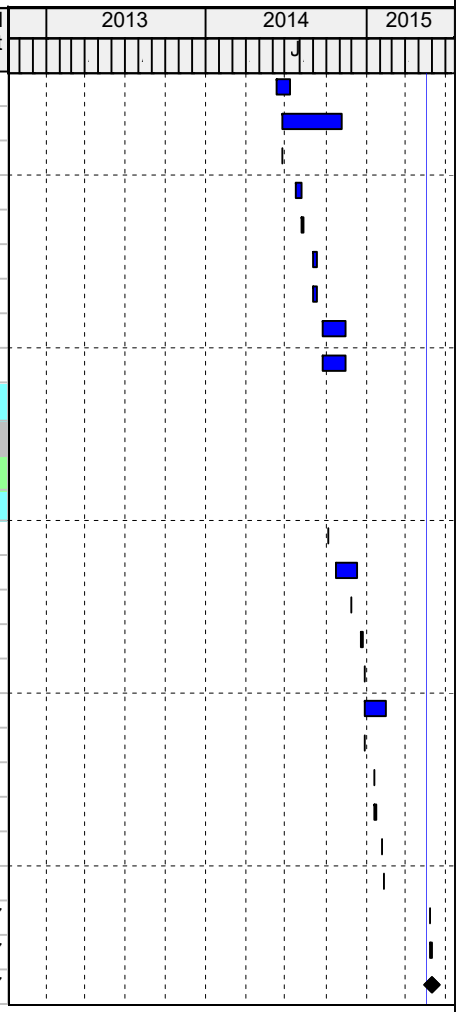


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL3-8100 | LL3 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| LL3-8102 | LL3 - GWB Hang (incl. screw inspection) | 3 | 0 | 27-Oct-14 A | 10-Dec-14 A | |
| LL3-8114 | LL3 - Striping / Signage [DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL3-8104 | LL3 - Int Painting | 3 | 0 | 22-Dec-14 A | 24-Dec-14 A | |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL3-8108 | Electrical trim & finish | 5 | 0 | 29-Dec-14 A | 16-Feb-15 A | |
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL3-8126 | Install doors & hardware | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL3-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 22-Jan-15 A | 03-Feb-15 A | |
| LL3-8124 | Flooring - VCT | 4 | 0 | 06-Feb-15 A | 07-Feb-15 A | |
| LL3-8110 | HVAC trim | 2 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| LL3-8134 | Final Cleaning | 2 | 2 | 26-May-15 | 27-May-15 | 7 |
| LL3-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 28-May-15 | 01-Jun-15 | 7 |
| LL3-8214 | LL3 Floor Complete | 0 | 0 | | 01-Jun-15 | 7 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL2E-8102 | LL2 - GWB Hang / Tape / Finish @ Electrical Rooms | 8 | 0 | 24-Jun-14 A | 03-Jul-14 A | |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish & Inspection | 6 | 0 | 16-Sep-14 A | 22-Dec-14 A | |
| LL2-8100 | LL2 - Insulation | 5 | 0 | 16-Sep-14 A | 09-Oct-14 A | |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 5 | 0 | 17-Sep-14 A | 27-Oct-14 A | |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| LL2-8104 | LL2 - Int Painting | 5 | 0 | 25-Nov-14 A | 23-Dec-14 A | |
| LL2-8114 | LL2 - Striping / Signage [DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL2-8116 | LL2 - Finish Carpentry / Millwork [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL2-8124 | Flooring - VCT | 4 | 0 | 06-Feb-15 A | 10-Mar-15 A | |

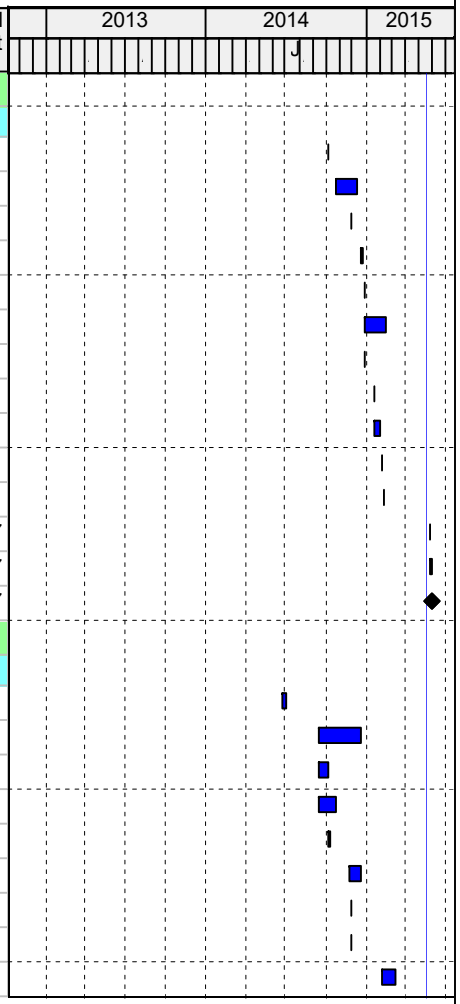



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-8126 | Install doors & hardware | 3 | 0 | 09-Feb-15 A | 16-Feb-15 A | |
| LL2-8122 | Complete MEP trim | 2 | 0 | 08-May-15 A | 08-May-15 A | |
| LL2-8136 | Chainlink Fencing / Gate @ Recycling at Garage | 5 | 5 | 26-May-15 | 01-Jun-15 | 3 |
| LL2-8120 | Install bollards at Garage | 5 | 5 | 26-May-15 | 01-Jun-15 | 3 |
| LL2-8128 | Entry Gates at Garage | 3 | 3 | 29-May-15 | 02-Jun-15 | 2 |
| LL2-8134 | Final Cleaning | 2 | 2 | 04-Jun-15 | 05-Jun-15 | 0 |
| LL2-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 08-Jun-15 | 10-Jun-15 | 0 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 31-Jul-14 A | |
| LL1-Z2U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 09-May-14 A | |
| LL1-Z3U-8102 | Above Ceiling GWB (At All Areas North of Q-Line) | 5 | 0 | 10-Feb-14 A | 20-Jun-14 A | |
| L1BU-8102 | Above Ceiling GWB [including East Service Corridor] | 5 | 0 | 06-Jun-14 A | 11-Jun-14 A | |
| L1LU-8102 | Above Ceiling GWB | 5 | 0 | 24-Jun-14 A | 13-Oct-14 A | |
| L1KU-8102 | Above Ceiling GWB | 2 | 0 | 26-Jun-14 A | 22-Aug-14 A | |
| LL1-8100 | Insulation | 5 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| LL1-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 28-Jul-14 A | 06-Aug-14 A | |
| LL1-Z2-8102 | GWB Hang (Walls) & Inspection | 4 | 0 | 11-Aug-14 A | 14-Aug-14 A | |
| LL1-Z2-8100 | Insulation | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| LL1-8215 | GWB Tape (Walls) | 10 | 0 | 16-Aug-14 A | 07-Nov-14 A | |
| LL1-Z3-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 15-Sep-14 A | 07-Oct-14 A | |
| LL1-Z3-8100 | Insulation | 5 | 0 | 15-Sep-14 A | 24-Sep-14 A | |
| LL1-Z2-8215 | GWB Tape (Walls/Ceilings) | 7 | 0 | 29-Sep-14 A | 07-Nov-14 A | |
| L1B-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L1K-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| LL1-Z3-8215 | GWB Tape (Walls & Ceilings) | 7 | 0 | 07-Oct-14 A | 18-Nov-14 A | |
| L1K-8102 | GWB Hang (Walls) & Inspection | 8 | 0 | 09-Oct-14 A | 31-Oct-14 A | |

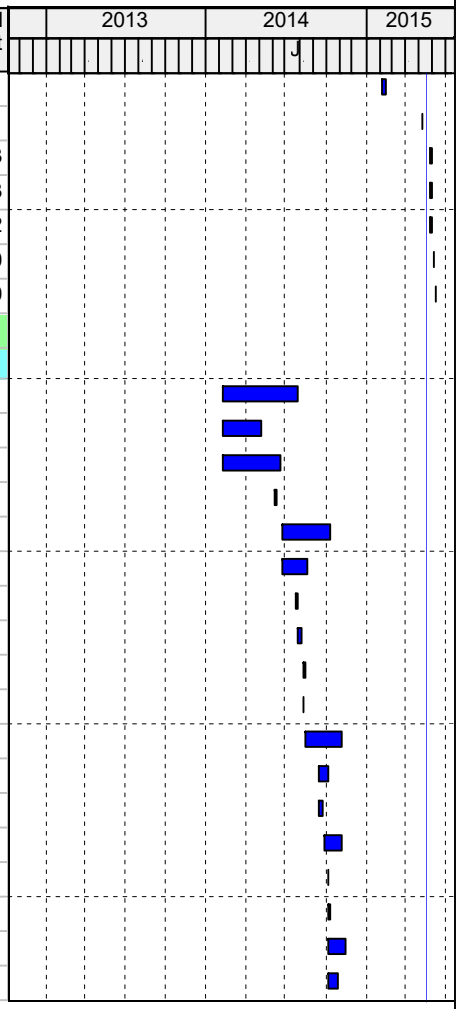



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8100 | Insulation | 4 | 0 | 13-Oct-14 A | 16-Oct-14 A | |
| L1B-8102 | GWB Hang (Walls) & Inspection - Main Ballroom N/S/ | 4 | 0 | 16-Oct-14 A | 22-Oct-14 A | |
| L1L-8102 | GWB hang walls (Dining & Lounge) | 4 | 0 | 30-Oct-14 A | 05-Feb-15 A | |
| L1K-8215 | GWB Tape (Walls & Ceilings) | 4 | 0 | 05-Nov-14 A | 18-Nov-14 A | |
| LL1-Z3-8104 | Prime Paint | 4 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| LL1-8104 | Prime Paint & First Coat Finish Paint | 5 | 0 | 02-Dec-14 A | 12-Dec-14 A | |
| L1K-8106 | Wall coverings - FRP | 8 | 0 | 19-Dec-14 A | 08-Jan-15 A | |
| LL1-Z3-8114 | Ceiling grid & inspection | 4 | 0 | 13-Jan-15 A | 16-Jan-15 A | |
| LL1-8126 | Install doors & hardware | 5 | 0 | 26-Jan-15 A | 03-Feb-15 A | |
| L1L-8215 | GWB hang ceilings (Dining & Lounge) | 5 | 0 | 29-Jan-15 A | 05-Feb-15 A | |
| LL1-8116 | Finish carpentry/millwork | 10 | 0 | 05-Feb-15 A | 02-Mar-15 A | |
| L1K-8114 | Ceiling grid & inspection (east end) | 8 | 0 | 05-Feb-15 A | 13-Mar-15 A | |
| LL1-Z3-8126 | Install doors & hardware | 5 | 0 | 09-Feb-15 A | 12-Feb-15 A | |
| L1K-8124 | Flooring - VCT | 3 | 0 | 10-Feb-15 A | 24-Apr-15 A | |
| LL1-8114 | Ceiling grid & inspection | 4 | 0 | 11-Feb-15 A | 20-Feb-15 A | |
| LL1-8118 | Lighting & electrical drops to grid | 3 | 0 | 12-Feb-15 A | 20-Feb-15 A | |
| LL1-Z2-8104 | Paint, prime at Jr. Ballrooms | 2 | 0 | 12-Feb-15 A | 13-Feb-15 A | |
| L1L-8104 | Paint, prime | 2 | 0 | 13-Feb-15 A | 17-Feb-15 A | |
| LL1-Z2-8126 | Install doors & hardware | 3 | 0 | 16-Feb-15 A | 06-Apr-15 A | |
| LL1-8112 | Fire sprinkler drops to grid | 2 | 0 | 17-Feb-15 A | 20-Feb-15 A | |
| LL1-Z2-8106 | Wall coverings - vinyl at Jr. Ballrooms | 2 | 0 | 18-Feb-15 A | 19-Feb-15 A | |
| LL1-Z2-8114 | Ceiling grid & inspection | 5 | 0 | 18-Feb-15 A | 26-Feb-15 A | |
| L1L-8114 | Install 9-wood ceiling supports - north of Grid K | 3 | 0 | 19-Feb-15 A | 26-Feb-15 A | |
| LL1-Z2-8116 | Finish carpentry/millwork | 10 | 0 | 20-Feb-15 A | 02-Mar-15 A | |
| L1K-8104 | Paint, prime | 2 | 0 | 26-Feb-15 A | 27-Feb-15 A | |
| L1B-8104 | Paint, prime & first coat finish | 3 | 0 | 06-Mar-15 A | 10-Mar-15 A | |
| LL1-Z2-8124 | Flooring - VCT at service corridor | 2 | 0 | 09-Mar-15 A | 11-Mar-15 A | |

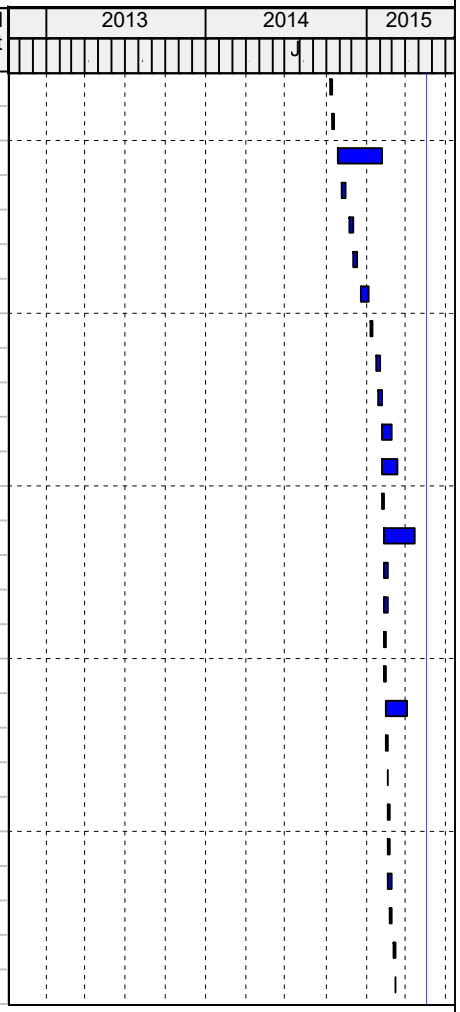


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8124 | Flooring - epoxy at Food Prep (including prep) | 6 | 0 | 09-Mar-15 A | 13-Mar-15 A | |
| LL1-Z2-8112 | Fire sprinkler drops to grid | 2 | 0 | 16-Mar-15 A | 31-Mar-15 A | |
| LL1-Z2-8118 | Lighting & electrical drops to grid | 3 | 0 | 16-Mar-15 A | 30-Mar-15 A | |
| LL1-Z3-8118 | Lighting & electrical drops at ceiling | 3 | 0 | 16-Mar-15 A | 18-Mar-15 A | |
| LL1-Z3-8112 | Fire sprinkler drops/trim at ceiling | 2 | 0 | 17-Mar-15 A | 28-Apr-15 A | |
| L1L-8140 | Install 9-wood ceiling - north of Grid K | 4 | 0 | 19-Mar-15 A | 31-Mar-15 A | |
| L1L-8116 | Finish carpentry/millwork - north of Grid K | 5 | 0 | 23-Mar-15 A | 27-Mar-15 A | |
| L1L-8126 | Install doors & hardware | 2 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| LL1-8124 | Flooring - VCT at storage areas, janitorial, mechanica | 3 | 0 | 25-Mar-15 A | 26-Mar-15 A | |
| L1B-8126 | Install doors & hardware at Ballrooms | 2 | 0 | 25-Mar-15 A | 13-Apr-15 A | |
| L1L-8112 | Fire sprinkler trim - north of Grid K | 1 | 0 | 31-Mar-15 A | 31-Mar-15 A | |
| L1K-8116 | Finish carpentry/millwork | 2 | 0 | 06-Apr-15 A | 06-Apr-15 A | |
| L1K-8126 | Install doors & hardware | 3 | 0 | 07-Apr-15 A | 08-Apr-15 A | |
| L1K-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8106 | Wall coverings - vinyl | 5 | 0 | 09-Apr-15 A | 27-Apr-15 A | |
| L1B-8116 | Finish carpentry/millwork at Ballrooms | 5 | 0 | 13-Apr-15 A | 17-Apr-15 A | |
| L1L-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 13-Apr-15 A | 13-Apr-15 A | |
| L1B-8114 | Ceiling grid & inspection | 3 | 0 | 15-Apr-15 A | 22-Apr-15 A | |
| LL1-Z3-8116 | Install VCT base | 3 | 1 | 29-Apr-15 A | 18-May-15 | 4 |
| L1L-8124 | Flooring - wood - north of Grid K | 4 | 3 | 11-May-15 A | 20-May-15 | -2 |
| L1K-8112 | Fire sprinkler trim | 1 | 0 | 12-May-15 A | 12-May-15 A | |
| LL1-Z2-8140 | Complete acoustical ceiling tile | 2 | 2 | 18-May-15 | 19-May-15 | 5 |
| LL1-Z3-8140 | Complete acoustical ceiling tile | 2 | 2 | 18-May-15 | 19-May-15 | 3 |
| L1B-8124 | Flooring - carpet at Ballrooms | 5 | 5 | 20-May-15 | 27-May-15 | -3 |
| L1B-8164 | Ceiling grid & inspection at Prefunction 2 | 2 | 2 | 26-May-15 | 27-May-15 | -4 |
| LL1-8134 | Final Cleaning | 2 | 2 | 28-May-15 | 29-May-15 | 5 |
| LL1-Z3-8134 | Final Cleaning | 2 | 2 | 28-May-15 | 29-May-15 | 5 |

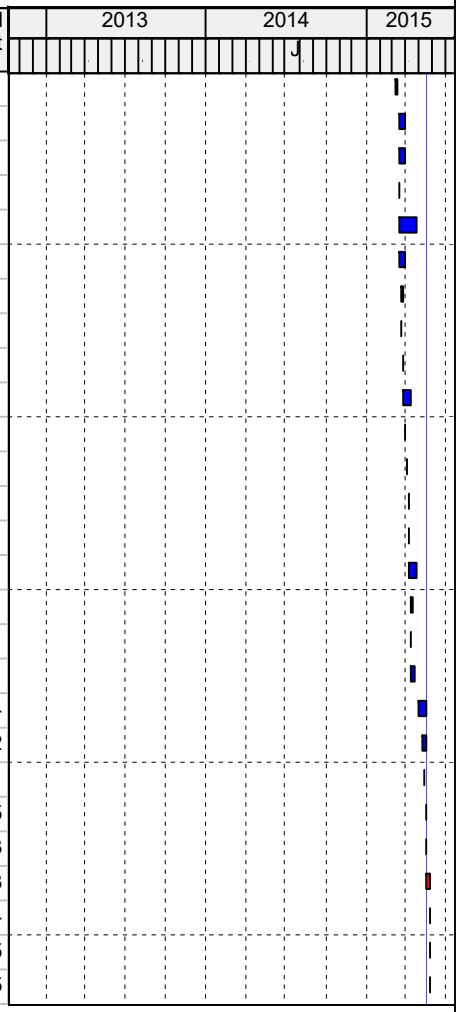


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-8140 | Complete acoustical ceiling tile | 2 | 2 | 28-May-15 | 29-May-15 | -2 |
| LL1-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 01-Jun-15 | 03-Jun-15 | 5 |
| LL1-Z3-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 01-Jun-15 | 03-Jun-15 | 5 |
| LL1-Z2-8134 | Final Cleaning | 2 | 2 | 02-Jun-15 | 03-Jun-15 | 2 |
| LL1-Z2-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 04-Jun-15 | 08-Jun-15 | 2 |
| L1K-8134 | Final Cleaning | 2 | 2 | 04-Jun-15 | 05-Jun-15 | 0 |
| L1L-8134 | Final Cleaning | 2 | 2 | 05-Jun-15 | 08-Jun-15 | -1 |
| L1K-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 08-Jun-15 | 10-Jun-15 | 0 |
| L1L-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 09-Jun-15 | 11-Jun-15 | -1 |
| L1B-8134 | Final Cleaning | 2 | 2 | 10-Jun-15 | 11-Jun-15 | -4 |
| L1B-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 12-Jun-15 | 16-Jun-15 | -4 |
| **Corridors / Common / Public Areas** | | | | | | |
| LL1-8200 | Wall coverings - vinyl | 4 | 0 | 17-Dec-14 A | 19-Jan-15 A | |
| LL1-Z3-8200 | Paint, first coat finish | 4 | 0 | 07-Jan-15 A | 12-Jan-15 A | |
| LL1-Z3-8204 | HVAC drops/trim at ceiling | 2 | 0 | 02-Feb-15 A | 17-Mar-15 A | |
| LL1-8204 | HVAC drops/trim to grid | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| LL1-Z2-8200 | Paint, first coat finish at Jr. Ballrooms | 1 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| L1L-8200 | Paint, first coat finish | 2 | 0 | 18-Feb-15 A | 18-Feb-15 A | |
| L1K-8200 | Paint, first coat finish | 1 | 0 | 02-Mar-15 A | 02-Mar-15 A | |
| LL1-Z2-8204 | HVAC drops/trim to grid | 2 | 0 | 16-Mar-15 A | 17-Mar-15 A | |
| L1L-8204 | HVAC trim at ceiling - north of Grid K | 1 | 0 | 27-Mar-15 A | 14-Apr-15 A | |
| L1B-8200 | Paint ceiling clouds | 3 | 0 | 02-Apr-15 A | 03-Apr-15 A | |
| L1K-8204 | HVAC drops/trim at ceiling | 1 | 0 | 20-Apr-15 A | 20-Apr-15 A | |
| L1B-8201 | Complete paint final coat & touch-up | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| LL1-8214 | LL1, Zone 1 Complete | 0 | 0 | | 03-Jun-15 | 5 |
| LL1-Z3-8214 | LL1, Zone 3 Complete | 0 | 0 | | 03-Jun-15 | 5 |
| LL1-Z2-8214 | LL1 Zone 2 Complete | 0 | 0 | | 08-Jun-15 | 2 |

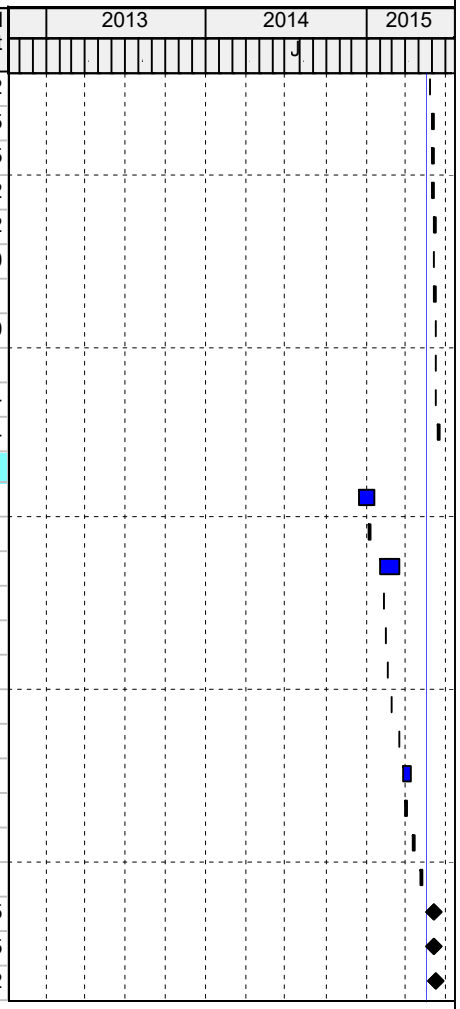


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8214 | L1, Zone 1 Complete | 0 | 0 | | 10-Jun-15 | 0 |
| L1L-8214 | L1, Zone 4 Complete | 0 | 0 | | 11-Jun-15 | -1 |
| L1B-8214 | L1, Zone 2 Complete | 0 | 0 | | 16-Jun-15 | -4 |
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8100 | L2 - Insulation - North Half | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L02-8102 | L2 - GWB Hang / Tape / Finish - North Half | 7 | 0 | 23-Oct-14 A | 17-Dec-14 A | |
| L02-8126 | Install doors & hardware at south half | 5 | 0 | 23-Mar-15 A | 15-Apr-15 A | |
| L02-8112 | Fire sprinkler drops/trim at south half | 2 | 0 | 01-Apr-15 A | 12-May-15 A | |
| L02-8120 | Ceramic tile | 15 | 0 | 02-Apr-15 A | 22-Apr-15 A | |
| L02-8104 | Paint, prime & first coat finish at north half | 2 | 0 | 03-Apr-15 A | 09-Apr-15 A | |
| L02-8106 | Wall coverings - vinyl at south half | 4 | 0 | 07-Apr-15 A | 14-Apr-15 A | |
| L02-8110 | HVAC drops/trim at south half | 2 | 0 | 15-Apr-15 A | 04-May-15 A | |
| L02-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 15-Apr-15 A | 16-Apr-15 A | |
| L02-8108 | Complete MEP trim (DELETED) | 2 | 0 | 01-May-15 A | 01-May-15 A | |
| L02-8122 | Plumbing fixtures & trim | 4 | 3 | 13-May-15 A | 20-May-15 | 1 |
| L02-8124 | Flooring - carpet | 4 | 4 | 19-May-15* | 22-May-15 | 0 |
| L02-8128 | Install bathroom accessories | 3 | 3 | 21-May-15 | 26-May-15 | 1 |
| L02-8136 | Lockers / Benches @ Locker Rooms | 3 | 3 | 21-May-15 | 26-May-15 | 1 |
| L02-8116 | Install base | 2 | 2 | 26-May-15 | 27-May-15 | 0 |
| L02-8134 | Final Cleaning | 2 | 2 | 04-Jun-15 | 05-Jun-15 | 0 |
| L02-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 08-Jun-15 | 10-Jun-15 | 0 |
| **Corridors** | | | | | | |
| L02-8200 | Complete paint final coat & touch-up (DELETED) | 2 | 0 | 01-May-15 A | 01-May-15 A | |
| L02-8214 | Floor Complete | 0 | 0 | | 10-Jun-15 | 0 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |

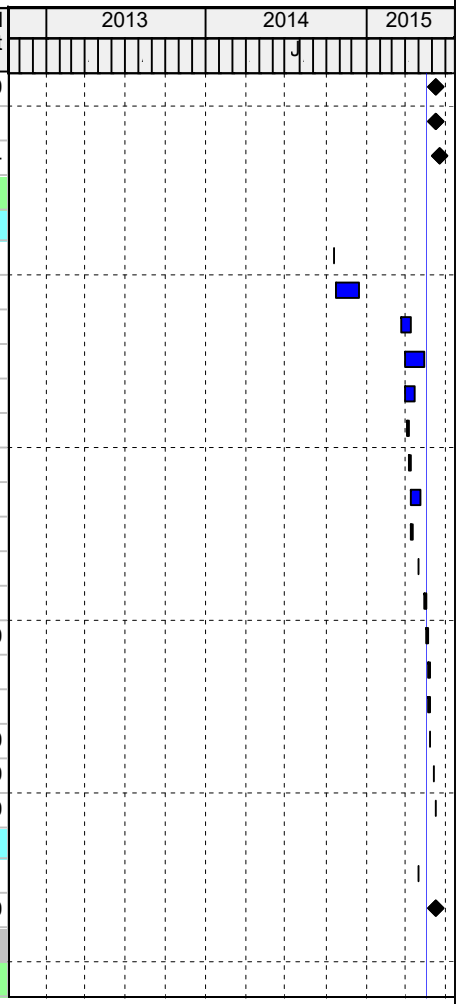



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Guest Rooms** | | | | | | |
| L03-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L04-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L05-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L06-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L07-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L08-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L09-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L10-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L11-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L12-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L14-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L15-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L16-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L17-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L03-8102S | Stock GWB | 2 | 0 | 27-Jun-14 A | 08-Jul-14 A | |
| L04-8102 | Hang GWB & Inspection | 4 | 0 | 07-Jul-14 A | 16-Jul-14 A | |
| L04-8102S | Stock GWB | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-8102 | Hang GWB & Inspection | 5 | 0 | 09-Jul-14 A | 22-Jul-14 A | |
| L05-8102S | Stock GWB | 2 | 0 | 10-Jul-14 A | 14-Jul-14 A | |
| L05-8102 | Hang GWB & Inspection | 4 | 0 | 17-Jul-14 A | 23-Jul-14 A | |
| L06-8102S | Stock GWB | 2 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L04-8104 | Paint (Prime) | 2 | 0 | 28-Jul-14 A | 05-Aug-14 A | |
| L03-8104 | Paint (Prime) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L03-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L07-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L08-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |

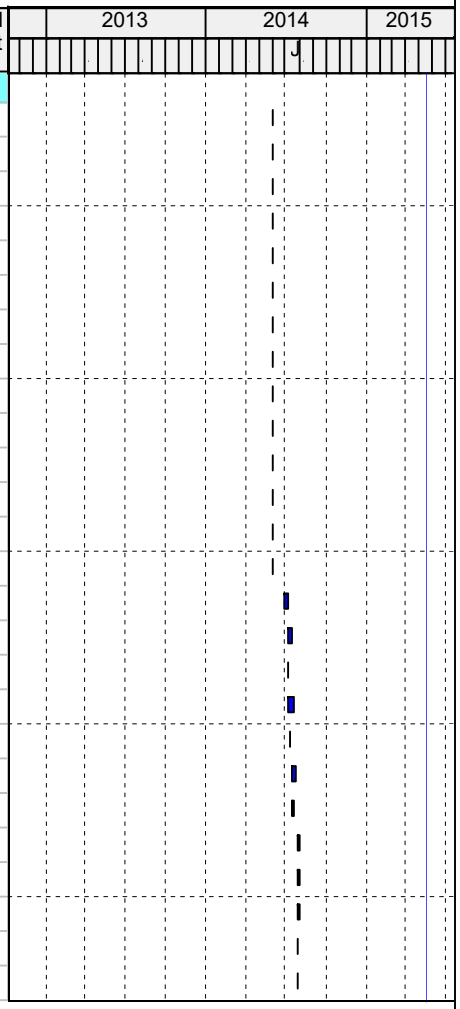



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8102 | Hang GWB & Inspection | 5 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L07-8102 | Hang GWB & Inspection | 6 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L04-8105 | Paint (First Coat & Ceilings) | 5 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L05-8104 | Paint (Prime) | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| L09-8102S | Stock GWB | 2 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 07-Aug-14 A | 11-Aug-14 A | |
| L09-8102 | Hang GWB & Inspection | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| L08-8102 | Hang GWB & Inspection | 6 | 0 | 11-Aug-14 A | 15-Aug-14 A | |
| L06-8104 | Paint (Prime) | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L10-8102S | Stock GWB | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-8102 | Hang GWB & Inspection | 4 | 0 | 13-Aug-14 A | 18-Aug-14 A | |
| L06-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 14-Aug-14 A | 18-Aug-14 A | |
| L11-8102S | Stock GWB | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L07-8104 | Paint (Prime) | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L11-8102 | Hang GWB & Inspection | 4 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| L07-8105 | Paint (First Coat & Ceilings) | 4 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L09-8104 | Paint (Prime) | 2 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L08-8104 | Paint (Prime) | 2 | 0 | 22-Aug-14 A | 25-Aug-14 A | |
| L12-8102 | Hang GWB & Inspection | 4 | 0 | 22-Aug-14 A | 30-Aug-14 A | |
| L12-8102S | Stock GWB | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8108 | Elec Trim / Finish | 4 | 0 | 25-Aug-14 A | 04-Sep-14 A | |
| L08-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L03-8118 | Fire Alarm Trim / Finish | 3 | 0 | 27-Aug-14 A | 29-Sep-14 A | |
| L14-8102S | Stock GWB | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L09-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 29-Aug-14 A | 09-Sep-14 A | |
| L14-8102 | Hang GWB & Inspection | 5 | 0 | 29-Aug-14 A | 05-Sep-14 A | |
| L03-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 02-Sep-14 A | 05-Sep-14 A | |

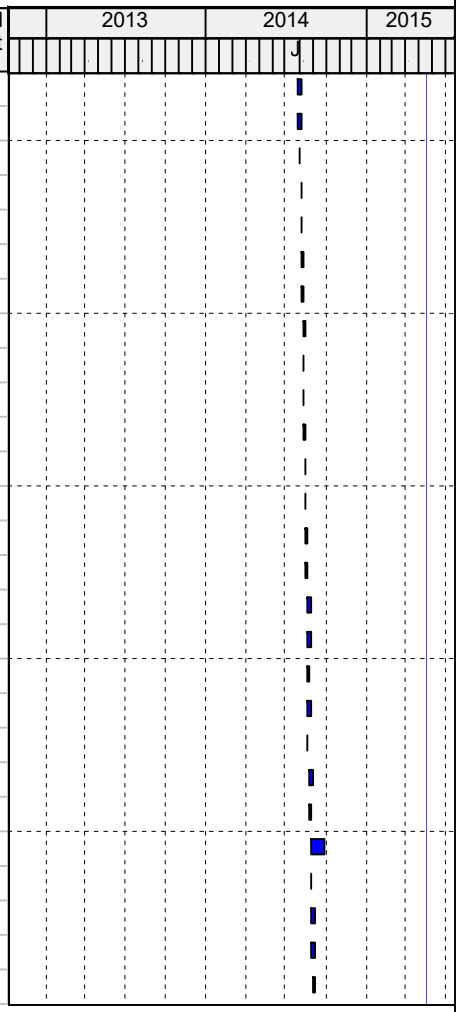



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 04-Sep-14 A | 09-Sep-14 A | |
| L10-8104 | Paint (Prime) | 2 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| L15-8102S | Stock GWB | 1 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L15-8102 | Hang GWB & Inspection | 5 | 0 | 06-Sep-14 A | 12-Sep-14 A | |
| L03-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8108 | Elec Trim / Finish | 4 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L04-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 11-Sep-14 A | |
| L05-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 08-Sep-14 A | 12-Sep-14 A | |
| L10-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 08-Sep-14 A | 12-Sep-14 A | |
| L11-8104 | Paint (Prime) | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L04-8116 | Install Base at Guestrooms | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L11-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 10-Sep-14 A | 22-Sep-14 A | |
| L03-8116 | Install Base at Guestrooms | 5 | 0 | 12-Sep-14 A | 16-Sep-14 A | |
| L12-8104 | Paint (Prime) | 2 | 0 | 12-Sep-14 A | 17-Sep-14 A | |
| L05-8116 | Install Base at Guestrooms | 5 | 0 | 16-Sep-14 A | 24-Sep-14 A | |
| L06-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L05-8108 | Elec Trim / Finish | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L07-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 17-Sep-14 A | 23-Sep-14 A | |
| L12-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 17-Sep-14 A | 06-Oct-14 A | |
| L06-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L07-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L14-8104 | Paint (Prime) | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L06-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L06-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |

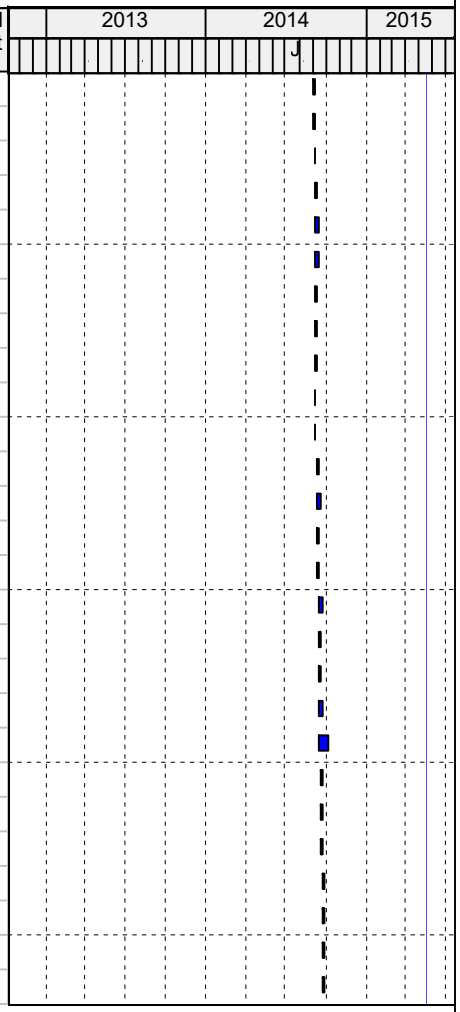



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L14-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 24-Sep-14 A | 06-Oct-14 A | |
| L15-8104 | Paint (Prime) | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L03-8110 | HVAC Grilles & Registers | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L03-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8118 | Fire Alarm Trim / Finish | 3 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L10-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L08-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 30-Sep-14 A | 06-Oct-14 A | |
| L03-8126 | Install Doors | 3 | 0 | 01-Oct-14 A | 07-Oct-14 A | |
| L03-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 01-Oct-14 A | 28-Oct-14 A | |
| L04-8126 | Install Doors | 3 | 0 | 02-Oct-14 A | 09-Oct-14 A | |
| L08-8116 | Install Base at Guestrooms | 5 | 0 | 02-Oct-14 A | 08-Oct-14 A | |
| L04-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8118 | Fire Alarm Trim / Finish | 3 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8108 | Elec Trim / Finish | 4 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L15-8105 | Paint - First Coast & Ceilings | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8126 | Install Doors | 3 | 0 | 08-Oct-14 A | 10-Oct-14 A | |
| L09-8116 | Install Base and Door Thresholds | 5 | 0 | 08-Oct-14 A | 15-Oct-14 A | |
| L09-8124 | Install Flooring | 5 | 0 | 08-Oct-14 A | 14-Oct-14 A | |
| L16-8102S | Stock GWB | 1 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L09-8112 | Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 10-Oct-14 A | |
| L16-8102 | Hang GWB & Inspection | 4 | 0 | 10-Oct-14 A | 17-Oct-14 A | |
| L06-8118 | Fire Alarm Trim / Finish | 3 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L09-8108 | Lighting and Electrical Trim | 3 | 0 | 13-Oct-14 A | 15-Oct-14 A | |
| L10-8124 | Install Flooring | 5 | 0 | 13-Oct-14 A | 16-Oct-14 A | |

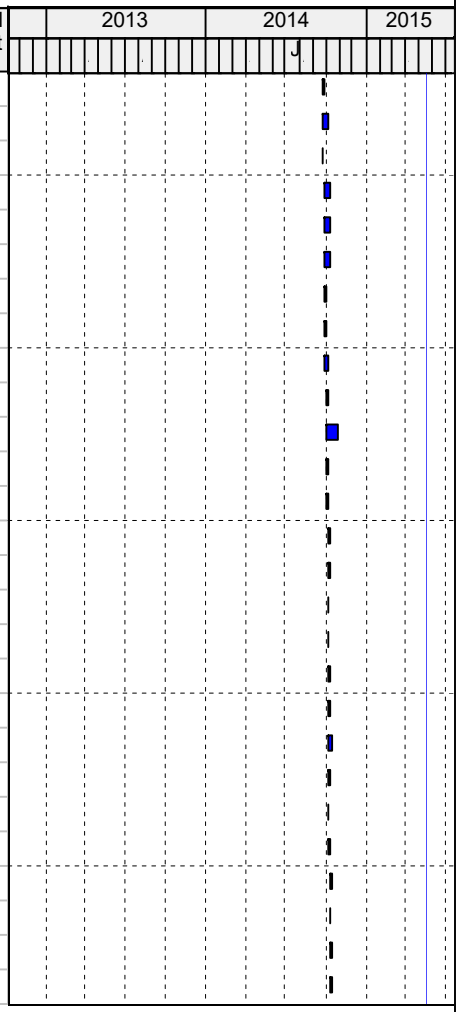



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8112 | Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L03-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 14-Oct-14 A | 04-Nov-14 A | |
| L06-8110 | HVAC Grilles & Registers | 2 | 0 | 14-Oct-14 A | 21-Oct-14 A | |
| L06-8126 | Install Doors | 2 | 0 | 14-Oct-14 A | 20-Oct-14 A | |
| L07-8118 | Fire Alarm Trim / Finish | 3 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L12-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L14-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L08-8118 | Fire Alarm Trim / Finish | 3 | 0 | 15-Oct-14 A | 16-Oct-14 A | |
| L10-8116 | Install Base and Door Thresholds | 5 | 0 | 15-Oct-14 A | 23-Oct-14 A | |
| L15-8112 | Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 16-Oct-14 A | |
| L04-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 16-Oct-14 A | 11-Nov-14 A | |
| L11-8124 | Install Flooring | 5 | 0 | 16-Oct-14 A | 22-Oct-14 A | |
| L17-8102S | Stock GWB | 1 | 0 | 17-Oct-14 A | 17-Oct-14 A | |
| L07-8126 | Install Doors | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |
| L09-8118 | Fire Alarm Trim | 2 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| L05-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 21-Oct-14 A | 14-Nov-14 A | |
| L08-8126 | Install Doors | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L10-8118 | Fire Alarm Trim | 2 | 0 | 21-Oct-14 A | 21-Oct-14 A | |
| L09-8126 | Install Doors | 2 | 0 | 22-Oct-14 A | 23-Oct-14 A | |
| L11-8118 | Fire Alarm Trim | 2 | 0 | 22-Oct-14 A | 22-Oct-14 A | |
| L06-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 23-Oct-14 A | 19-Nov-14 A | |
| L10-8126 | Install Doors | 2 | 0 | 23-Oct-14 A | 27-Oct-14 A | |
| L12-8124 | Install Flooring | 5 | 0 | 23-Oct-14 A | 29-Oct-14 A | |
| L12-8118 | Fire Alarm Trim | 2 | 0 | 23-Oct-14 A | 23-Oct-14 A | |
| L11-8116 | Install Base and Door Thresholds | 5 | 0 | 24-Oct-14 A | 26-Nov-14 A | |
| L07-8110 | HVAC Grilles & Registers | 2 | 0 | 27-Oct-14 A | 28-Oct-14 A | |
| L10-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |

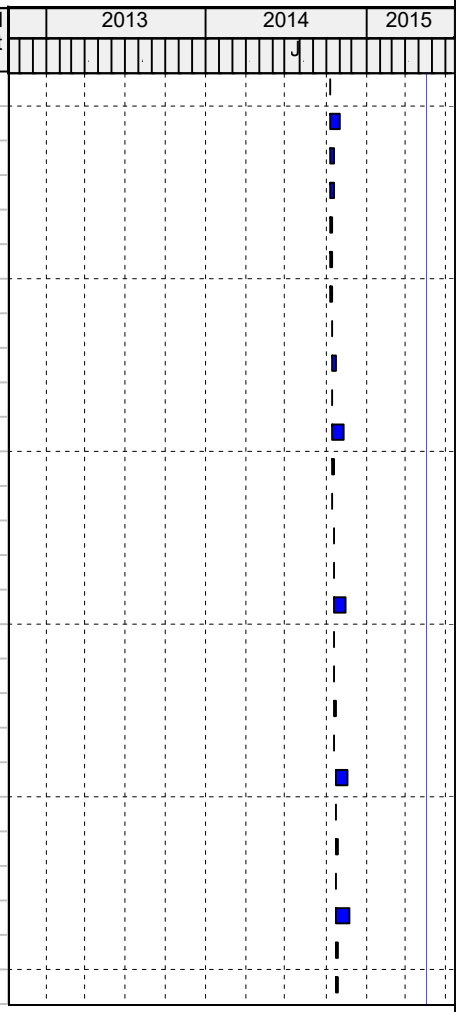



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |
| L17-8102 | Hang GWB & Inspection | 4 | 0 | 27-Oct-14 A | 03-Nov-14 A | |
| L07-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 28-Oct-14 A | 26-Nov-14 A | |
| L08-8120 | Bathrooms - Install Countertops | 3 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L11-8126 | Install Doors | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L12-8108 | Lighting and Electrical Trim | 3 | 0 | 28-Oct-14 A | 30-Oct-14 A | |
| L12-8116 | Install Base and Door Thresholds | 5 | 0 | 28-Oct-14 A | 03-Dec-14 A | |
| L14-8118 | Fire Alarm Trim | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L05-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Oct-14 A | 31-Oct-14 A | |
| L06-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Oct-14 A | 31-Oct-14 A | |
| L12-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L14-8108 | Lighting and Electrical Trim | 3 | 0 | 29-Oct-14 A | 03-Nov-14 A | |
| L14-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8118 | Fire Alarm Trim | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L04-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 30-Oct-14 A | 04-Nov-14 A | |
| L07-8120 | Bathrooms - Install Countertops | 3 | 0 | 03-Nov-14 A | 05-Nov-14 A | |
| L08-8110 | HVAC Grilles & Registers | 2 | 0 | 03-Nov-14 A | 04-Nov-14 A | |
| L09-8120 | Bathrooms - Install Countertops | 3 | 0 | 03-Nov-14 A | 05-Nov-14 A | |
| L10-8120 | Bathrooms - Install Countertops | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| L15-8108 | Lighting and Electrical Trim | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| L11-8120 | Bathrooms - Install Countertops | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| L16-8104 | Paint - Prime | 2 | 0 | 05-Nov-14 A | 06-Nov-14 A | |
| L05-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 07-Nov-14 A | 12-Nov-14 A | |
| L16-8105 | Paint - First Coat & Ceilings | 3 | 0 | 07-Nov-14 A | 11-Nov-14 A | |
| L12-8120 | Bathrooms - Install Countertops | 3 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L14-8124 | Install Flooring | 5 | 0 | 10-Nov-14 A | 14-Nov-14 A | |

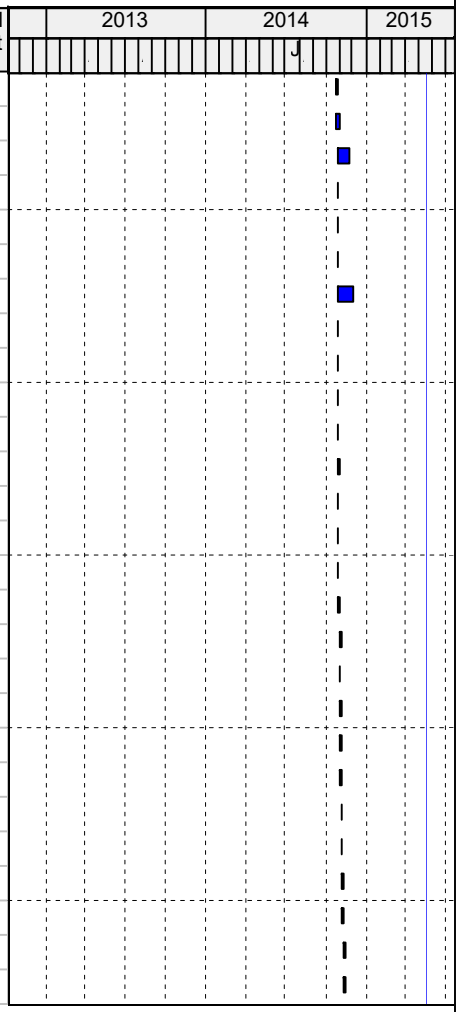



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 13-Nov-14 A | 17-Nov-14 A | |
| L15-8124 | Install Flooring | 5 | 0 | 17-Nov-14 A | 25-Nov-14 A | |
| L17-8104 | Paint - Prime | 2 | 0 | 17-Nov-14 A | 18-Nov-14 A | |
| L14-8116 | Install Base and Door Thresholds | 5 | 0 | 18-Nov-14 A | 08-Dec-14 A | |
| L16-8126 | Install Doors | 2 | 0 | 18-Nov-14 A | 19-Nov-14 A | |
| L07-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 19-Nov-14 A | 25-Nov-14 A | |
| L15-8116 | Install Base and Door Thresholds | 5 | 0 | 20-Nov-14 A | 08-Dec-14 A | |
| L03-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L04-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L05-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L08-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| L17-8105 | Paint - First Coat & Ceilings | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L16-8124 | Install Flooring | 5 | 0 | 25-Nov-14 A | 03-Dec-14 A | |
| L16-8112 | Fire Sprinkler Trim | 2 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| L16-8118 | Fire Alarm Trim | 2 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| L06-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L07-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L08-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 01-Dec-14 A | 08-Dec-14 A | |
| L08-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L09-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 01-Dec-14 A | 10-Dec-14 A | |
| L16-8108 | Lighting and Electrical Trim | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L17-8126 | Install Doors | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| L16-8116 | Install Base and Door Thresholds | 5 | 0 | 02-Dec-14 A | 15-Dec-14 A | |
| L17-8112 | Fire Sprinkler Trim | 2 | 0 | 02-Dec-14 A | 02-Dec-14 A | |
| L09-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 03-Dec-14 A | 08-Dec-14 A | |
| L09-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L10-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |

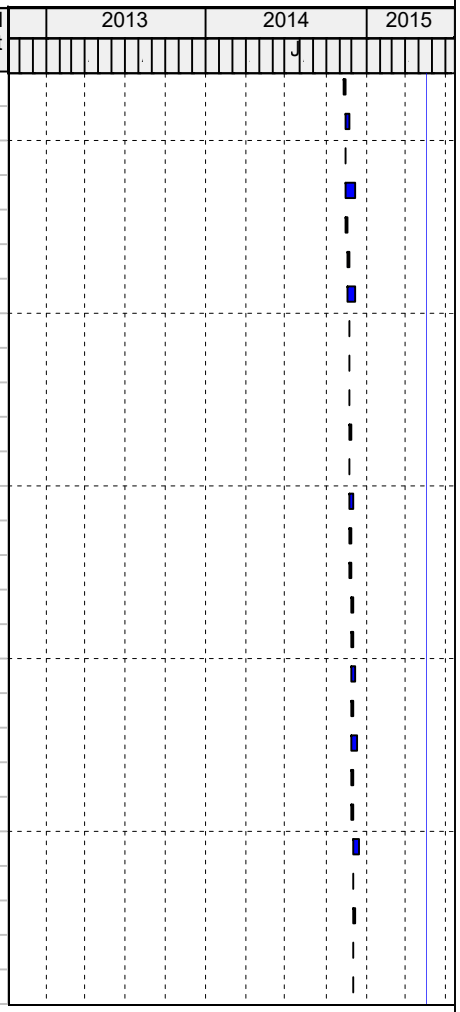



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L17-8118 | Fire Alarm Trim | 2 | 0 | 03-Dec-14 A | 03-Dec-14 A | |
| L12-8107 | Paint Final Coat | 3 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L14-8120 | Bathrooms - Install Countertops | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L17-8108 | Lighting and Electrical Trim | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L10-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L15-8120 | Bathrooms - Install Countertops | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 10-Dec-14 A | 16-Dec-14 A | |
| L11-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 10-Dec-14 A | 24-Dec-14 A | |
| L04-8132 | Contractor Punchlist (inspect/distribute/correct/back-pl | 7 | 0 | 11-Dec-14 A | 05-Feb-15 A | |
| L04-8134 | Final Clean @ Guestrooms | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L05-8132 | Contractor Punchlist (inspect/distribute/correct/back-pl | 7 | 0 | 12-Dec-14 A | 10-Feb-15 A | |
| L05-8134 | Final Clean @ Guestrooms | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L11-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 12-Dec-14 A | 17-Dec-14 A | |
| L06-8134 | Final Clean @ Guestrooms | 5 | 0 | 13-Dec-14 A | 13-Dec-14 A | |
| L12-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 15-Dec-14 A | 18-Dec-14 A | |
| L17-8124 | Install Flooring | 5 | 0 | 15-Dec-14 A | 18-Dec-14 A | |
| L17-8116 | Install Base and Door Thresholds | 5 | 0 | 18-Dec-14 A | 30-Dec-14 A | |
| L12-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| L14-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| L15-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 29-Dec-14 A | 05-Jan-15 A | |
| L16-8120 | Bathrooms - Install countertops | 3 | 0 | 29-Dec-14 A | 09-Jan-15 A | |
| L14-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 30-Dec-14 A | 05-Jan-15 A | |
| L15-8122 | Bathrooms - Plumbing fixtures & trim | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L16-8128 | Bathrooms - Install shower/tub surrounds | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L16-8122 | Bathrooms - Plumbing fixtures & trim | 3 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8128 | Bathrooms - Install shower/tub surrounds | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |

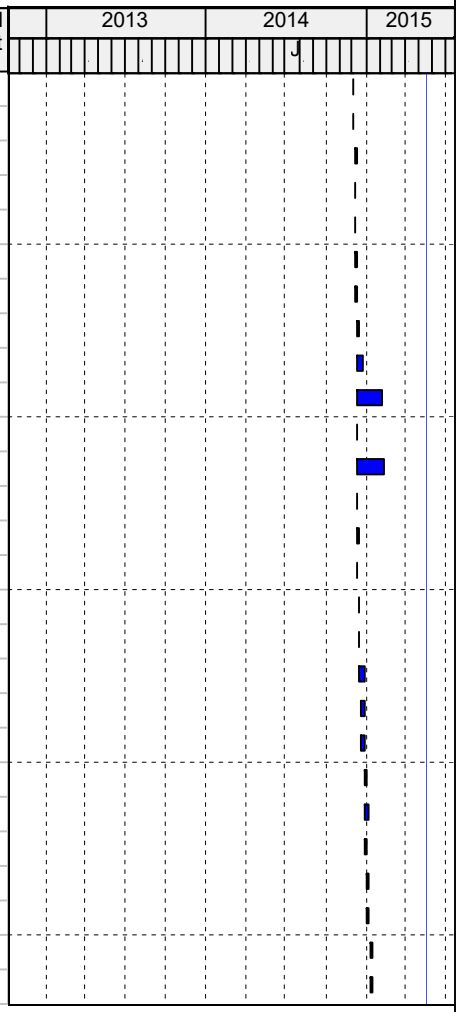



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8110 | HVAC grilles & registers | 2 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| L11-8110 | HVAC grilles & registers | 2 | 0 | 21-Jan-15 A | 28-Jan-15 A | |
| L12-8110 | HVAC grilles & registers | 2 | 0 | 21-Jan-15 A | 28-Jan-15 A | |
| L14-8110 | HVAC grilles & registers | 2 | 0 | 21-Jan-15 A | 02-Feb-15 A | |
| L10-8110 | HVAC grilles & registers | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L15-8110 | HVAC grilles & registers | 2 | 0 | 03-Feb-15 A | 16-Feb-15 A | |
| L16-8110 | HVAC grilles & registers | 2 | 0 | 03-Feb-15 A | 23-Feb-15 A | |
| L17-8122 | Bathrooms - Plumbing fixtures & trim | 3 | 0 | 03-Feb-15 A | 06-May-15 A | |
| L17-8120 | Bathrooms - Install countertops | 3 | 0 | 03-Feb-15 A | 24-Apr-15 A | |
| L06-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 04-Feb-15 A | 12-Feb-15 A | |
| L07-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 06-Feb-15 A | 20-Feb-15 A | |
| L14-8107 | Paint, final coat & touch-up | 3 | 0 | 09-Feb-15 A | 11-Feb-15 A | |
| L17-8110 | HVAC grilles & registers | 2 | 0 | 09-Feb-15 A | 31-Mar-15 A | |
| L08-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 10-Feb-15 A | 07-Mar-15 A | |
| L09-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 12-Feb-15 A | 06-Mar-15 A | |
| L15-8107 | Paint, final coat & touch-up | 3 | 0 | 16-Feb-15 A | 18-Feb-15 A | |
| L10-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 18-Feb-15 A | 13-Mar-15 A | |
| L11-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 20-Feb-15 A | 20-Mar-15 A | |
| L16-8107 | Paint, final coat & touch-up | 3 | 0 | 24-Feb-15 A | 26-Feb-15 A | |
| L12-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 25-Feb-15 A | 25-Mar-15 A | |
| L14-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 26-Feb-15 A | 27-Mar-15 A | |
| L03-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L04-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L05-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L06-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L07-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L08-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |

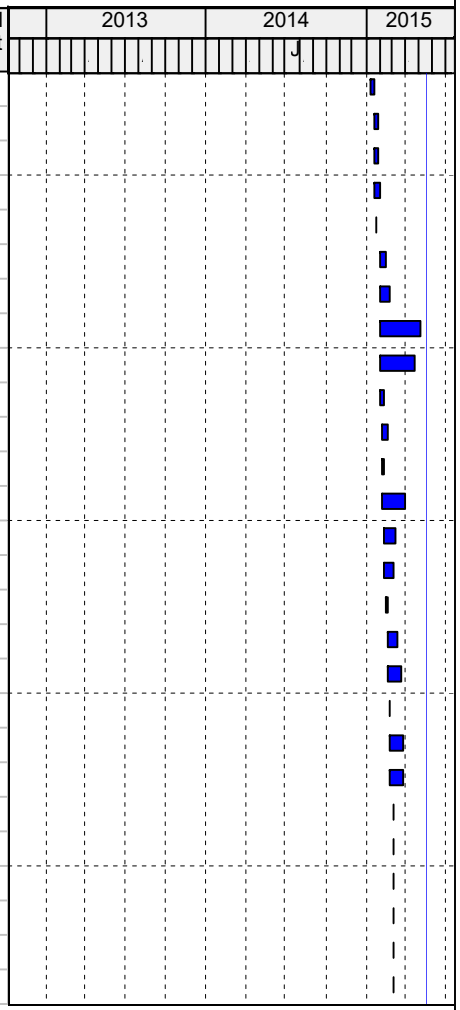



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L10-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L11-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L12-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L14-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L15-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L16-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L17-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L15-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 06-Mar-15 A | 06-Apr-15 A | |
| L16-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 10-Mar-15 A | 08-Apr-15 A | |
| L17-8107 | Paint, final coat & touch-up | 2 | 0 | 25-Mar-15 A | 26-Mar-15 A | |
| L03-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 0 | 13-Apr-15 A | 17-Apr-15 A | |
| L17-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 19-May-15 | 26-May-15 | 1 |
| **Pool Area** | | | | | | |
| L03-8216 | Install pool tile, coping and depth markers | 5 | 5 | 01-Jun-15 | 05-Jun-15 | 0 |
| **Corridors / Common / Public Areas** | | | | | | |
| L03-8200 | Vinyl Wall Coverings | 3 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L04-8200 | Vinyl Wall Coverings | 5 | 0 | 06-Aug-14 A | 12-Aug-14 A | |
| L05-8200 | Vinyl Wall Coverings | 5 | 0 | 12-Aug-14 A | 22-Sep-14 A | |
| L03-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L06-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L08-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 11-Sep-14 A | 19-Sep-14 A | |
| L04-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| L05-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L06-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L07-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |

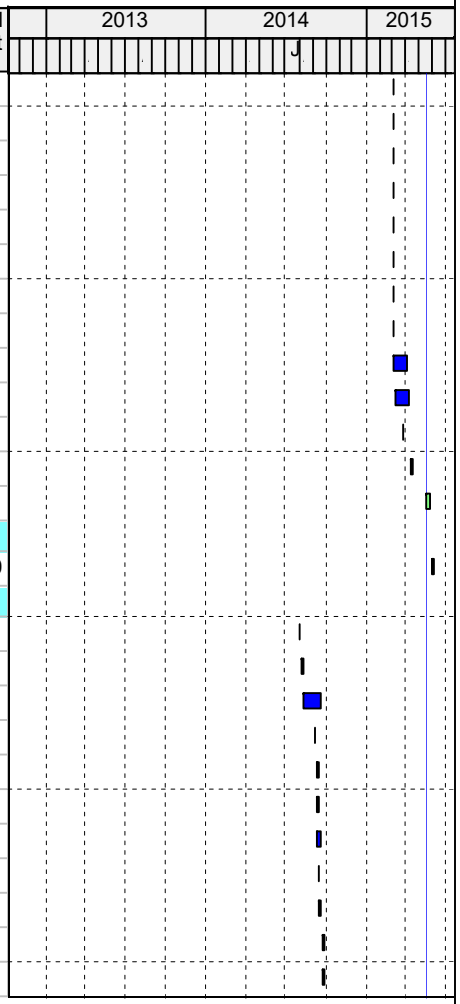


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| L10-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 08-Oct-14 A | |
| L11-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 10-Oct-14 A | |
| L08-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L12-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| L09-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L14-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 16-Oct-14 A | 27-Oct-14 A | |
| L10-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |
| L11-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L15-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 22-Oct-14 A | 29-Oct-14 A | |
| L12-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 03-Nov-14 A | 04-Nov-14 A | |
| L14-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L15-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 05-Nov-14 A | 06-Nov-14 A | |
| L16-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 14-Nov-14 A | 20-Nov-14 A | |
| L16-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L17-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L17-8200 | Wall coverings - vinyl at window niches & outside batl | 4 | 0 | 15-Dec-14 A | 24-Mar-15 A | |
| L04-8206 | Flooring - carpet at corridors | 2 | 0 | 14-Jan-15 A | 23-Jan-15 A | |
| L05-8206 | Flooring - carpet at corridors | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| L07-8206 | Flooring - carpet at corridors | 2 | 0 | 22-Jan-15 A | 23-Jan-15 A | |
| L06-8206 | Flooring - carpet at corridors | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L09-8206 | Flooring - carpet at corridors | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| L08-8206 | Flooring - carpet at corridors | 2 | 0 | 04-Feb-15 A | 05-Feb-15 A | |
| L10-8206 | Flooring - carpet at corridors | 2 | 0 | 06-Feb-15 A | 09-Feb-15 A | |
| L11-8206 | Flooring - carpet at corridors | 2 | 0 | 10-Feb-15 A | 11-Feb-15 A | |
| L12-8206 | Flooring - carpet at corridors | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| L04-8208 | Final Cleaning | 2 | 0 | 13-Feb-15 A | 16-Feb-15 A | |

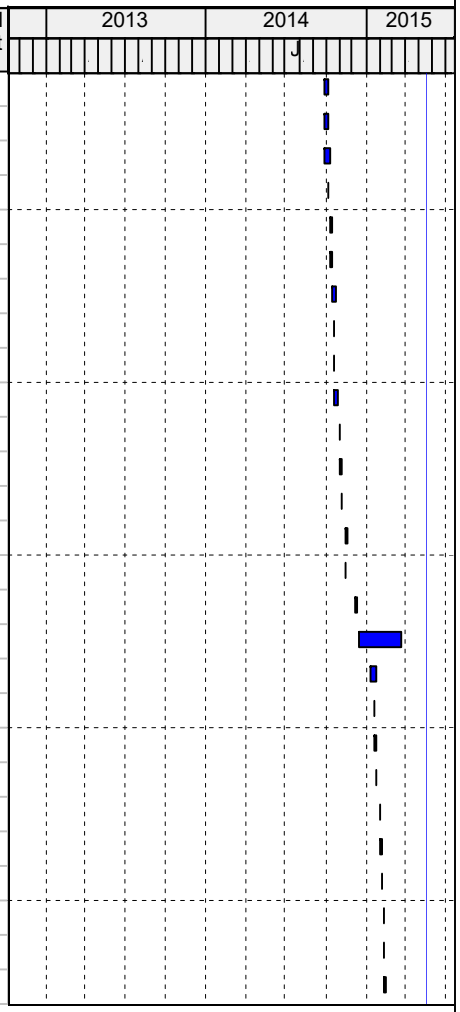



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8206 | Flooring - carpet at corridors | 2 | 0 | 13-Feb-15 A | 14-Feb-15 A | |
| L15-8206 | Flooring - carpet at corridors | 2 | 0 | 16-Feb-15 A | 17-Feb-15 A | |
| L04-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 17-Feb-15 A | 03-Mar-15 A | |
| L05-8208 | Final Cleaning | 2 | 0 | 17-Feb-15 A | 18-Feb-15 A | |
| L05-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 18-Feb-15 A | 05-Mar-15 A | |
| L16-8206 | Flooring - carpet at corridors | 2 | 0 | 18-Feb-15 A | 19-Feb-15 A | |
| L06-8208 | Final Cleaning | 2 | 0 | 20-Feb-15 A | 25-Feb-15 A | |
| L03-8206 | Flooring - carpet at corridors (N-S leg) | 2 | 0 | 25-Feb-15 A | 25-Feb-15 A | |
| L06-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 4 | 0 | 25-Feb-15 A | 10-Mar-15 A | |
| L07-8208 | Final Cleaning | 2 | 0 | 27-Feb-15 A | 02-Mar-15 A | |
| L04-8214 | Floor Complete | 0 | 0 | | 03-Mar-15 A | |
| L07-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 05-Mar-15 A | 18-Mar-15 A | |
| L08-8208 | Final Cleaning | 2 | 0 | 05-Mar-15 A | 06-Mar-15 A | |
| L05-8214 | Floor Complete | 0 | 0 | | 05-Mar-15 A | |
| L08-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 06-Mar-15 A | 25-Mar-15 A | |
| L06-8214 | Floor Complete | 0 | 0 | | 10-Mar-15 A | |
| L09-8208 | Final Cleaning | 2 | 0 | 12-Mar-15 A | 13-Mar-15 A | |
| L09-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 12-Mar-15 A | 25-Mar-15 A | |
| L07-8214 | Floor Complete | 0 | 0 | | 18-Mar-15 A | |
| L10-8208 | Final Cleaning | 2 | 0 | 19-Mar-15 A | 20-Mar-15 A | |
| L10-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 9 | 0 | 23-Mar-15 A | 06-Apr-15 A | |
| L11-8208 | Final Cleaning | 2 | 0 | 23-Mar-15 A | 24-Mar-15 A | |
| L11-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 8 | 0 | 24-Mar-15 A | 06-Apr-15 A | |
| L08-8214 | Floor Complete | 0 | 0 | | 25-Mar-15 A | |
| L09-8214 | Floor Complete | 0 | 0 | | 25-Mar-15 A | |
| L12-8208 | Final Cleaning | 2 | 0 | 26-Mar-15 A | 27-Mar-15 A | |
| L12-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 9 | 0 | 31-Mar-15 A | 09-Apr-15 A | |

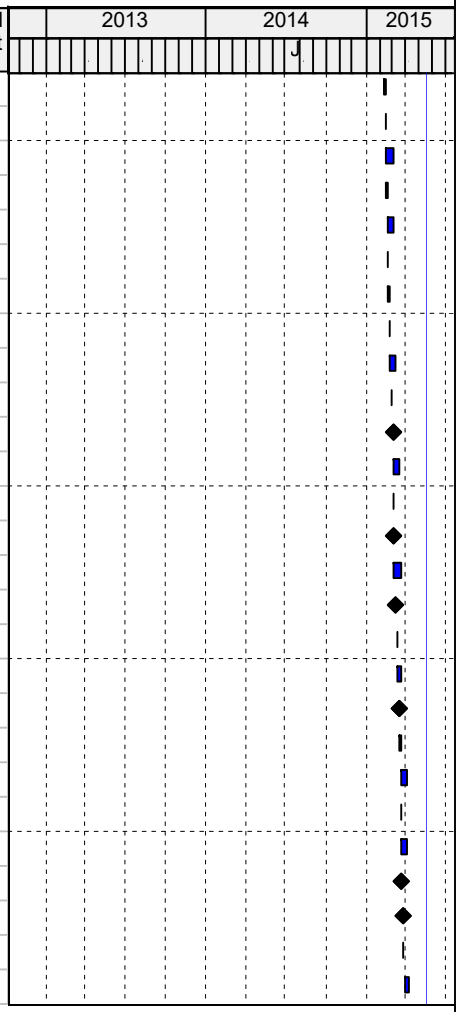



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-8208 | Final Cleaning | 2 | 0 | 31-Mar-15 A | 01-Apr-15 A | |
| L17-8206 | Flooring - carpet at corridors | 2 | 0 | 31-Mar-15 A | 01-Apr-15 A | |
| L14-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 7 | 0 | 06-Apr-15 A | 09-Apr-15 A | |
| L15-8208 | Final Cleaning | 2 | 0 | 06-Apr-15 A | 07-Apr-15 A | |
| L10-8214 | Floor Complete | 0 | 0 | | 06-Apr-15 A | |
| L11-8214 | Floor Complete | 0 | 0 | | 06-Apr-15 A | |
| L15-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 9 | 0 | 08-Apr-15 A | 16-Apr-15 A | |
| L16-8208 | Final Cleaning | 2 | 0 | 09-Apr-15 A | 10-Apr-15 A | |
| L12-8214 | Floor Complete | 0 | 0 | | 09-Apr-15 A | |
| L14-8214 | Floor Complete | 0 | 0 | | 09-Apr-15 A | |
| L16-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 7 | 0 | 10-Apr-15 A | 16-Apr-15 A | |
| L15-8214 | Floor Complete | 0 | 0 | | 16-Apr-15 A | |
| L16-8214 | Floor Complete | 0 | 0 | | 16-Apr-15 A | |
| L03-8208 | Final Cleaning | 2 | 0 | 22-Apr-15 A | 27-Apr-15 A | |
| L03-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 29-Apr-15 A | 07-May-15 A | |
| L17-8208 | Final Cleaning | 2 | 2 | 27-May-15 | 28-May-15 | 1 |
| L17-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 7 | 7 | 28-May-15 | 05-Jun-15 | 1 |
| L17-8214 | Floor Complete | 0 | 0 | | 05-Jun-15 | 1 |
| L03-8214 | Floor Complete | 0 | 0 | | 10-Jul-15 | 0 |
| **Mech Penthouse** | | | | | | |
| PH-8100 | PH - Insulation & Vapor Barrier | 5 | 0 | 09-Oct-14 A | 13-Oct-14 A | |
| PH-8102 | PH - Complete GWB Hang / Tape / Finish | 6 | 0 | 14-Oct-14 A | 10-Nov-14 A | |
| PH-8122 | PH - Plumbing Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8110 | PH - HVAC Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8126 | PH - install doors & hardware | 2 | 0 | 24-Nov-14 A | 23-Feb-15 A | |
| PH-8104 | PH - Int Painting [DELETED] | 4 | 0 | 01-Dec-14 A | 01-Dec-14 A | |

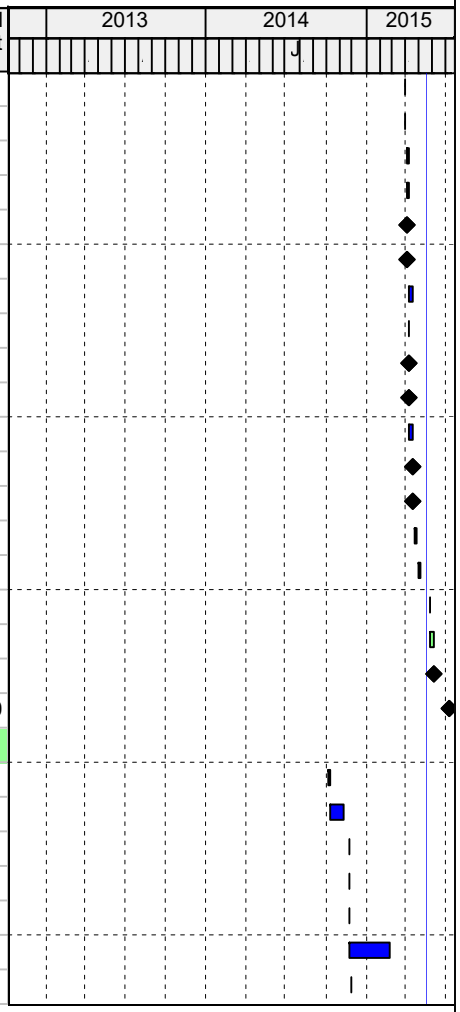


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-8108 | PH - Elec Trim / Finish | 5 | 0 | 01-Dec-14 A | 19-Jan-15 A | |
| PH-8114 | PH - Install Stairs to Roof [DELETED] | 1 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| PH-8118 | PH - Fire Alarm Trim (speaker/strobe & smoke detecto | 5 | 0 | 01-Dec-14 A | 21-Jan-15 A | |
| PH-8124 | PH - Flooring [DELETED, NIC] | 5 | 0 | 01-Jan-15 A | 01-Jan-15 A | |
| PH-8134 | PH - Final Trims and Touch-Up | 3 | 0 | 16-Mar-15 A | 18-Mar-15 A | |
| PH-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 0 | 20-Apr-15 A | 24-Apr-15 A | |
| PH-8208 | Final Cleaning | 2 | 0 | 27-Apr-15 A | 28-Apr-15 A | |
| PH-8212 | Owner Punchlist (inspect/distribute/correct) | 3 | 0 | 29-Apr-15 A | 01-May-15 A | |
| PH-8214 | Penthouse Complete | 0 | 0 | | 01-May-15 A | |
| **Start-Up / Testing / Commissioning** | | | | | | |
| **Smoke Control** | | | | | | |
| CO-7104 | Fire Alarm/Smoke Control Pre-Functional Testing - Po | 9 | 9 | 18-May-15 | 29-May-15 | 1 |
| CO-7106 | City of Bellevue Smoke Control Functional Acceptanc | 5 | 5 | 01-Jun-15 | 05-Jun-15 | 1 |
| CO-7108 | Final Marriott Smoke Control Functional Acceptance T | 2 | 2 | 08-Jun-15 | 09-Jun-15 | 1 |
| **Fire Sprinklers** | | | | | | |
| CO-7114 | Marriott Fire Sprinkler Funcational Acceptance Testing | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7110 | Fire Sprinkler Pre-Testing (Podium) | 3 | 0 | 26-Mar-15 A | 26-Mar-15 A | |
| CO-7112 | City of Bellevue Fire Sprinkler Final Inspection | 5 | 5 | 01-Jun-15 | 05-Jun-15 | 1 |
| **Fire Alarm** | | | | | | |
| CO-7116 | Fire Alarm Pre-Testing (Podium) [DELETED] | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7118 | City of Bellevue Fire Alarm Functional Acceptance Tes | 5 | 5 | 01-Jun-15 | 05-Jun-15 | 1 |
| CO-7120 | Marriott Fire Alarm Functional Acceptance Testing | 2 | 2 | 08-Jun-15 | 09-Jun-15 | 1 |
| **Start-Up / Testing / Commissioning** | | | | | | |
| CO-7100 | Cx - Start-Up - Garage Exhaust Fan and VFD's | 4 | 0 | 30-Mar-15 A | 02-Apr-15 A | |
| CO-7102 | Cx - DDC Point-To-Point - Garage Exhaust Fans [DEL | 5 | 0 | 01-Apr-15 A | 01-Apr-15 A | |

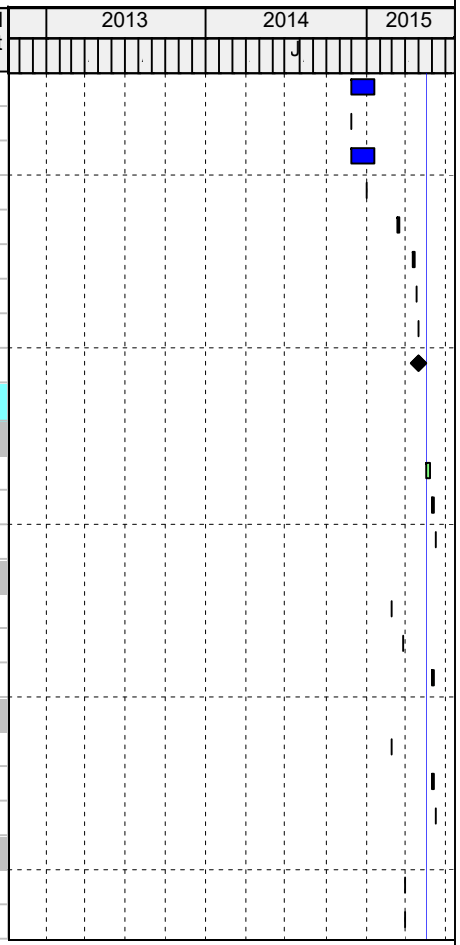



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Marriott Hotel - Bellevue, WA - Working Schedule - 6-14-15 Update** | | | | | | |
| I-4500 | Re-design building exterior (change from EIFS panels | 30 | 0 | 12-Apr-13 A | 28-May-14 A | |
| ASI01 | ASI No. 1 - Tower Crane Foundation Changes | 0 | 0 | 09-May-13 A | | |
| I-2292 | RFI 233/ Original HVAC submittal with specified damp | 1 | 0 | 13-May-13 A | 12-Jun-13 A | |
| ASI03 | ASI No. 3 - Food Service Plans and Cut Sheets | 0 | 0 | 14-May-13 A | | |
| ASI04 | ASI No. 4 - Revised Structural For The Podium | 0 | 0 | 22-May-13 A | | |
| ASI05 | ASI No. 5 - NTI Drawings | 0 | 0 | 22-May-13 A | | |
| I-1500 | Owner release revised LV design - Tower (ASIs 5, 13, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| I-1550 | Owner release revised LV design - Podium (ASIs 5, 1 | 200 | 0 | 23-May-13 A | 28-Apr-14 A | |
| I-1900 | Owner issue design revisions (ASIs 4, 9, 19, 34) | 215 | 0 | 23-May-13 A | 24-Mar-14 A | |
| I-2500 | Owner issue LL1 electrical revisions (ASIs 7, 9r2, 14, | 200 | 0 | 23-May-13 A | 09-Apr-14 A | |
| ASI02 | ASI No. 2 - Foundation Drainage System | 0 | 0 | 05-Jun-13 A | | |
| ASI04c | ASI No. 4 - Revised Structural For The Podium (Clouc | 0 | 0 | 05-Jun-13 A | | |
| ASI07 | ASI No. 7 - Electrical Rev-10 Changes | 0 | 0 | 18-Jun-13 A | | |
| ASI06 | ASI No. 6 - Mechanical Rev-8 Changes | 0 | 0 | 19-Jun-13 A | | |
| I-3700 | Owner resolve wall condition between stair and Eleva | 200 | 0 | 27-Jun-13 A | 16-Jun-14 A | |
| MM-1000 | MM - Temporary Power Available | 0 | 0 | 08-Jul-13 A | | |
| I-2100 | Owner revise roof steel design (Submittals 365, 370, | 200 | 0 | 09-Jul-13 A | 07-Apr-14 A | |
| I-2200 | Owner resolve elevator steel issue (RFI 112, RFI 112. | 200 | 0 | 09-Jul-13 A | 03-Mar-14 A | |
| I-2400 | Owner provide Tower light fixture selections (ASI 36) | 185 | 0 | 18-Jul-13 A | 08-Apr-14 A | |
| I-3400 | Owner provide Level 2 ceiling heights (RFI 465) | 180 | 0 | 19-Jul-13 A | 01-Jul-14 A | |
| I-2294 | RFI 233/ Revised HVAC submittal | 1 | 0 | 22-Jul-13 A | 25-Jul-13 A | |
| ASI04ca | ASI No. 4 - Revised Structural For The Podium (City A | 0 | 0 | 05-Aug-13 A | | |
| ASI11 | ASI No. 11 - Food and Beverage Drawing Revisions | 0 | 0 | 05-Aug-13 A | | |
| I-2900 | Owner revise Food Service and Kitchen (ASIs 11, 12, | 140 | 0 | 08-Aug-13 A | 27-Feb-14 A | |
| ASI12 | ASI No. 12 - Food and Beverage Drawing Changes | 0 | 0 | 12-Aug-13 A | | |
| ASI08 | ASI No. 8 - Provent System | 0 | 0 | 15-Aug-13 A | | |

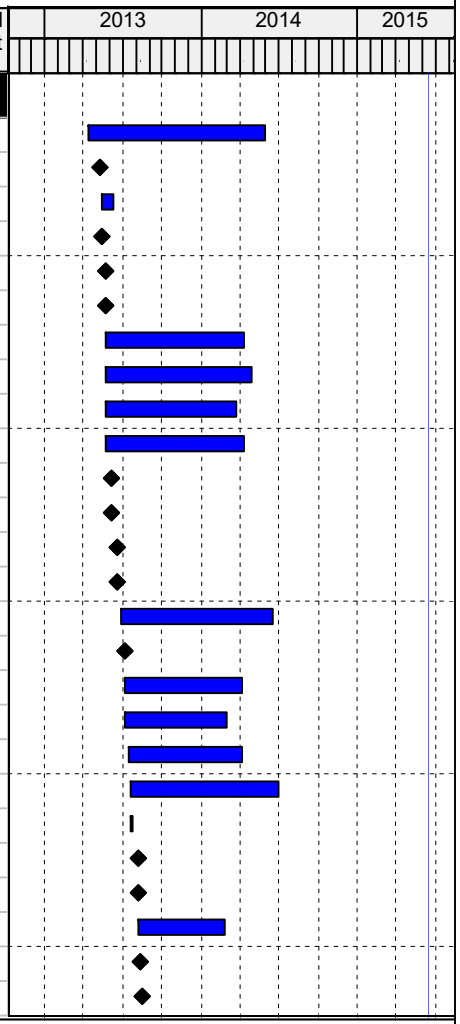


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-5010 | RFI 173 - Porte Cochere Bench Design | 1 | 0 | 16-Aug-13 A | 04-Sep-13 A | |
| I-5012 | RFI 189 - Porte Cochere Pavement Design | 1 | 0 | 26-Aug-13 A | 30-Jun-14 A | |
| I-1400 | Owner develop envelope redesign | 70 | 0 | 27-Aug-13 A | 12-Dec-13 A | |
| I-5014 | RFI 197 - LL1 & LL2 Planter Drain Pipes | 1 | 0 | 03-Sep-13 A | 06-Sep-13 A | |
| I-3600 | Owner closeout glass/glazing allowance | 160 | 0 | 04-Sep-13 A | 30-Apr-14 A | |
| ASI09 | ASI No. 9 - Incorporating Arch, MEP & Struct Drawing | 0 | 0 | 05-Sep-13 A | | |
| I-1200 | Owner release revised Concierge Lounge design (AS | 160 | 0 | 06-Sep-13 A | 22-Oct-14 A | |
| ASI13 | ASI No. 13 - NTI Drawing Updates | 0 | 0 | 06-Sep-13 A | | |
| I-2800 | Owner revise interior public space design (ASIs 16, 1 | 130 | 0 | 25-Sep-13 A | 09-Apr-14 A | |
| ASI16 | ASI No. 16 - 9.20..13 General ID Releasae | 0 | 0 | 25-Sep-13 A | | |
| I-2296 | RFI 233/ Issue RFI and receive response | 1 | 0 | 25-Sep-13 A | 21-Jan-14 A | |
| I-2000 | Owner approve door frames (Submittals 258, 454, 48 | 85 | 0 | 27-Sep-13 A | 23-Jan-14 A | |
| ASI14 | ASI No. 14 - Electrical Revisions for Low Voltage | 0 | 0 | 04-Oct-13 A | | |
| ASI17 | ASI No. 17 - Smoke Control Design 42C Permit | 0 | 0 | 09-Oct-13 A | | |
| ASI18 | ASI No. 18 - Interior Package Revisions | 0 | 0 | 15-Oct-13 A | | |
| I-3100 | Owner revise ballroom ceiling design (ASIs 18, 25) | 100 | 0 | 17-Oct-13 A | 25-Feb-14 A | |
| I-1600 | Owner provide directive for south & east corridor encl | 110 | 0 | 28-Oct-13 A | 18-Apr-14 A | |
| I-5016 | RFI 282 - Porte Cochere Planter Dimensions | 1 | 0 | 01-Nov-13 A | 21-Jan-14 A | |
| ASI11-12 | ASI No. 11 & 12 - Kitchen Equipment Specifications | 0 | 0 | 06-Nov-13 A | | |
| ASI09r1s | ASI No. 9 (Revised) - City Approved ASI No. 9 (Struct | 0 | 0 | 07-Nov-13 A | | |
| I-2600 | Owner resolve L2 slab coordination issue | 4 | 0 | 13-Nov-13 A | 16-Nov-13 A | |
| ASI09r1m | ASI No. 9 (Revised) - City Approved ASI No. 9 (Mecha | 0 | 0 | 15-Nov-13 A | | |
| ASI06r1 | ASI No. 6 (Revised) - Mechanical Rev-8 Changes (Cit | 0 | 0 | 19-Nov-13 A | | |
| ASI21 | ASI No. 21 - Revised Structural Drawings for the Roof | 0 | 0 | 22-Nov-13 A | | |
| I-2700 | Owner revise tower guest rooms design (ASIs 23, 29) | 58 | 0 | 04-Dec-13 A | 26-Feb-14 A | |
| ASI09r1e | ASI No. 9 (Revised) - ASI No. 9 Electrical Drawings (R | 0 | 0 | 04-Dec-13 A | | |
| ASI20 | ASI No. 20 - Dry Utilities Revisions | 0 | 0 | 05-Dec-13 A | | |

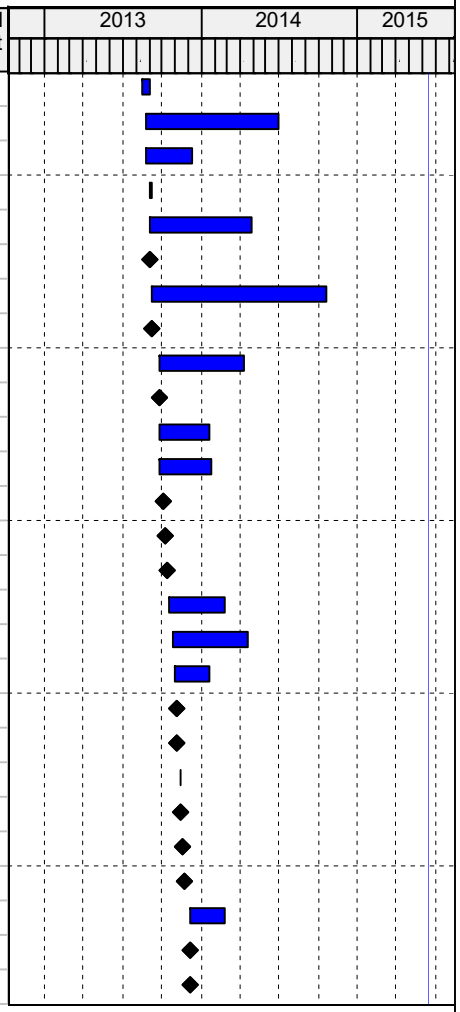


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| High Rise Hotel Sample Project | All Activities | Schedule Status Date 15-Jun-15 |
|---|---|---|

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1700 | Owner provide design for dry site utilities (ASIs 20, 20 | 66 | 0 | 09-Dec-13 A | 13-Mar-14 A | |
| I-1402 | Begin exterior panel production | 41 | 0 | 13-Dec-13 A | 12-Feb-14 A | |
| ASI17ca | ASI No. 17 - Smoke Control Design 42C Permit (City / | 0 | 0 | 16-Dec-13 A | | |
| ASI09r2e | ASI No. 9 (Revised) - ASI No. 9 Electrical Drawings (R | 0 | 0 | 18-Dec-13 A | | |
| I-1300 | Owner issue "Hold" directive (email) | 0 | 0 | | 19-Dec-13 A | |
| ASI22 | ASI No. 22 - Revised Door Schedule and Door Hardw | 0 | 0 | 19-Dec-13 A | | |
| I-1100 | Owner release revised L17 design (ASI 23, 29R1) | 74 | 0 | 20-Dec-13 A | 08-Apr-14 A | |
| I-1302 | Owner issue ASI 30 (Prep Kitchen Revisions) | 47 | 0 | 20-Dec-13 A | 27-Feb-14 A | |
| ASI23 | ASI No. 23 - Revised Tower and Enlarged Guestroom | 0 | 0 | 20-Dec-13 A | | |
| I-1404 | City of Bellevue Approval | 90 | 0 | 23-Dec-13 A | 15-Jul-14 A | |
| I-5470 | Resolve ceiling height issue at Laundy Room (RFI __ | 5 | 0 | 05-Jan-14 A | 30-Jan-15 A | |
| ASI15 | ASI No. 15 - NTI DV Drawings Revisions | 0 | 0 | 08-Jan-14 A | | |
| ASI09R2e2 | ASI No. 9 (Revised) - City Approved ASI No. 9 (Electri | 0 | 0 | 14-Jan-14 A | | |
| ASI22r1 | ASI No. 22 (Revised) - Architectural Revisions to Door | 0 | 0 | 20-Jan-14 A | | |
| I-3000 | ASI 38/ Owner revise bar area (change to straight bai | 71 | 0 | 22-Jan-14 A | 27-May-14 A | |
| I-2298 | RFI 233/ Resolve issue with designer & City | 1 | 0 | 22-Jan-14 A | 14-Mar-14 A | |
| ASI20r1 | ASI No. 20 (Revised) - Dry Utilities Revsions | 0 | 0 | 23-Jan-14 A | | |
| ASI24 | ASI No. 24 - FRCH ID Finish Schedule | 0 | 0 | 30-Jan-14 A | | |
| ASI26 | ASI No. 26 - Revised Laundry Layout and Equipment | 0 | 0 | 12-Feb-14 A | | |
| I-1306 | Prep Kitchen - Additional plumbing (ASI 30) | 4 | 0 | 17-Feb-14 A | 01-Aug-14 A | |
| ASI28 | ASI No. 28 - Guest Laundry Equipment Sheets | 0 | 0 | 20-Feb-14 A | | |
| ASI27 | ASI No. 27 - Mechanical, Electrical and Plumbing She | 0 | 0 | 21-Feb-14 A | | |
| ASI25 | ASI No. 25 - Podium Level Revisions (Stair 1 & 2 Gat | 0 | 0 | 24-Feb-14 A | | |
| ASI29 | ASI No. 29 - Architectural Tower and Guestroom Revi | 0 | 0 | 26-Feb-14 A | | |
| ASI30 | ASI No. 30 - Food Service Revisions per HEI | 0 | 0 | 27-Feb-14 A | | |
| I-2202 | Fabricate revised elevator steel | 60 | 0 | 04-Mar-14 A | 07-May-14 A | |
| I-2704 | Framing "Go Back" work for ASIs 23, 29 - L4 | 1 | 0 | 05-Mar-14 A | 12-Mar-14 A | |

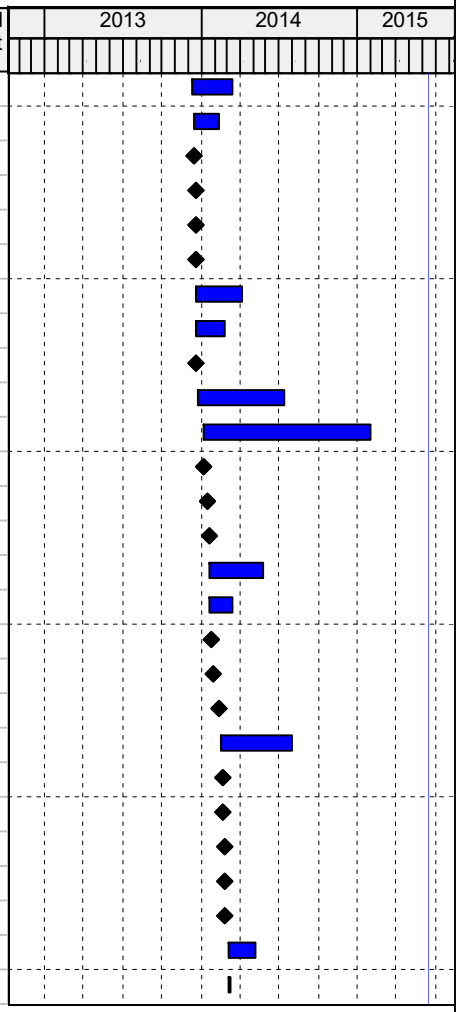


Actual Work
Remaining Work
Critical Remai...
Milestone



TASK filter: All Activities

© Oracle Corporation

| High Rise Hotel Sample Project | All Activities | Schedule Status Date 15-Jun-15 |
|---|---|---|

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ASI31 | ASI No. 31 - Revised Elevations | 0 | 0 | 07-Mar-14 A | | |
| ASI33 | ASI No. 33 - NTI DV Drawing Revisions | 0 | 0 | 11-Mar-14 A | | |
| ASI20r2 | ASI No. 20 (Revised) - Dry Utilities Revisions | 0 | 0 | 13-Mar-14 A | | |
| I-1702 | Owner provide directive to proceed | 26 | 0 | 14-Mar-14 A | 01-May-14 A | |
| I-2300 | RFI 233/ Procure dampers | 1 | 0 | 15-Mar-14 A | 11-Apr-14 A | |
| I-3300 | Owner provide Guest Room plumbing fixture selectio | 1 | 0 | 20-Mar-14 A | 20-Mar-14 A | |
| ASI34 | ASI No. 34 - SCA Structural Revisions S6.01 and S6.( | 0 | 0 | 24-Mar-14 A | | |
| I-4600 | RFI 72, HHP3-HHP5 - resolve electrical issue & revise | 1 | 0 | 24-Mar-14 A | 09-Apr-14 A | |
| I-1902 | Procure revised structural steel | 15 | 0 | 25-Mar-14 A | 14-Apr-14 A | |
| I-3900 | Ballroom Parapet Height Issue/ RFI 471 | 1 | 0 | 28-Mar-14 A | 07-May-14 A | |
| I-3016 | ASI 38/ Scan Level 1 slab at bar (3 times) | 1 | 0 | 31-Mar-14 A | 11-Apr-14 A | |
| I-4000 | Owner complete design of east stitched enclosure (fo | 1 | 0 | 01-Apr-14 A | 14-May-14 A | |
| ASI35 | ASI No. 35 - FRCH ID Revisions and Finish Schedule | 0 | 0 | 07-Apr-14 A | | |
| I-2102 | Fabricate revised roof steel | 20 | 0 | 08-Apr-14 A | 15-May-14 A | |
| I-3200 | Owner provide light fixture selections for podium level | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| ASI36 | ASI No. 36 - MDP Electrical Revisions Rev. 16 | 0 | 0 | 08-Apr-14 A | | |
| ASI29r1 | ASI No. 29 (Revised) - Guestroom, Interior Elevation, | 0 | 0 | 09-Apr-14 A | | |
| I-3800 | Resolve  Heat Pump Electrical Overcurrent Issue | 20 | 0 | 23-Apr-14 A | 18-Jun-14 A | |
| L10-8221 | HVAC Risers Duct Insulation | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L11-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-8221 | HVAC Risers Duct Insulation | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| ASI37 | ASI No. 37 - NTI DV Drawing Revisions | 0 | 0 | 28-Apr-14 A | | |
| I-2304 | RFI 233/ Framing "Go Back" work at L3 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2306 | RFI 233/ Framing "Go Back" work at L4 | 3 | 0 | 29-Apr-14 A | 07-May-14 A | |
| I-2308 | RFI 233/ Framing "Go Back" work at L5 | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2706 | Framing "Go Back" work for ASIs 23, 29 - L5 | 1 | 0 | 29-Apr-14 A | 13-May-14 A | |
| I-2708 | Framing "Go Back" work for ASIs 23, 29 - L6 | 1 | 0 | 29-Apr-14 A | 09-May-14 A | |

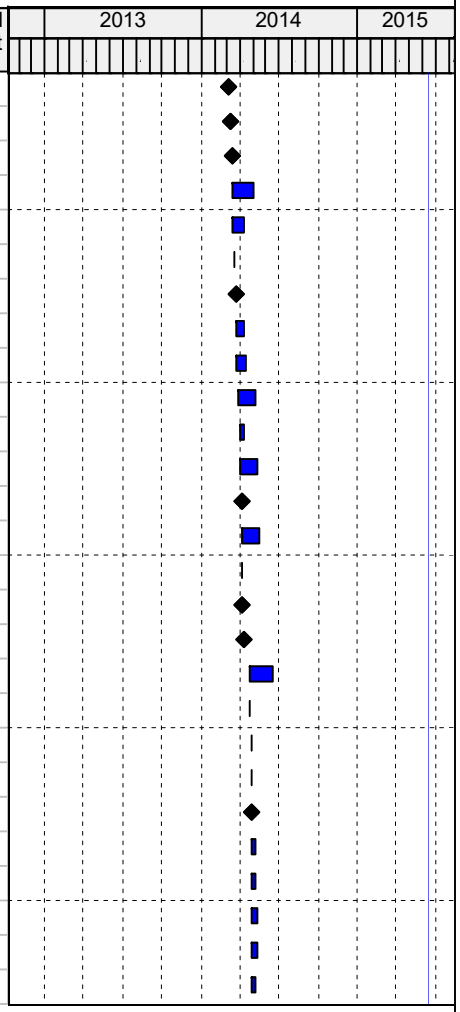


Actual Work  Critical Remai...
Remaining Work  Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-2702 | Framing "Go Back" work for ASIs 23, 29 - L3 | 1 | 0 | 01-May-14 A | 01-May-14 A | |
| I-1706 | PSE scheduling delay | 10 | 0 | 01-May-14 A | 20-May-14 A | |
| I-3602 | Complete shop drawings & fab/deliver storefront fram | 40 | 0 | 01-May-14 A | 14-Jun-14 A | |
| L04-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| I-3904 | Ballroom Parapet Height Issue/ re-engineer parapet | 1 | 0 | 06-May-14 A | 01-Jul-14 A | |
| I-1802 | Rework framing for door hold-opens - LL4 | 1 | 0 | 07-May-14 A | 08-May-14 A | |
| L04-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-May-14 A | 12-May-14 A | |
| ASI25r1 | ASI No. 25 (Revised) - Architectural Podium Level Re | 0 | 0 | 07-May-14 A | | |
| ASI29r2 | ASI No. 29 (Revised) - Architectural Tower and Guestı | 0 | 0 | 07-May-14 A | | |
| I-1800 | Owner issue directive to proceed with door hold-open | 1 | 0 | 08-May-14 A | 08-May-14 A | |
| I-1804 | Rework framing for door hold-opens - LL3 | 1 | 0 | 08-May-14 A | 09-May-14 A | |
| I-2312 | RFI 233/ Framing "Go Back" work at L7 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-2314 | RFI 233/ Framing "Go Back" work at L8 | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| I-3902 | Install Ballroom parapet extension | 5 | 0 | 08-May-14 A | 13-May-14 A | |
| I-1806 | Rework framing for door hold-opens - LL2 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-1808 | Rework framing for door hold-opens - LL1 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| I-2310 | RFI 233/ Framing "Go Back" work at L6 | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| I-2710 | Framing "Go Back" work for ASIs 23, 29 - L7 | 1 | 0 | 09-May-14 A | 12-May-14 A | |
| L05-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L06-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 09-May-14 A | 11-May-14 A | |
| L05-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 09-May-14 A | 13-May-14 A | |
| LL2E-8110 | LL2 - Electrical, Fire pumps/equipment final connectic | 5 | 0 | 12-May-14 A | 30-Oct-14 A | |
| I-2316 | RFI 233/ Install dampers | 1 | 0 | 12-May-14 A | 15-May-14 A | |
| PH-8704 | PH - Install Machine Support Steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| PH-8710 | Install elevator rail support steel | 3 | 0 | 13-May-14 A | 03-Jun-14 A | |
| L03-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 13-May-14 A | 14-May-14 A | |

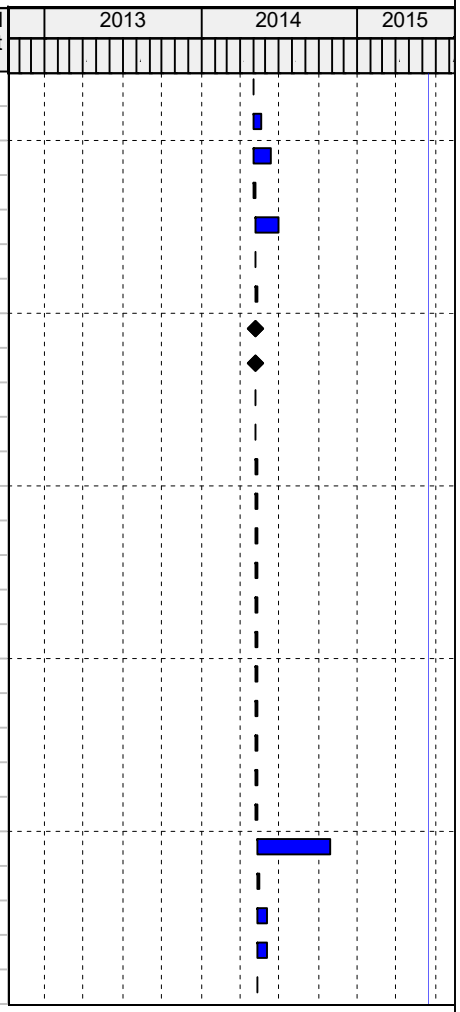



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 13-May-14 A | 14-May-14 A | |
| I-2318 | RFI 233/ Install dampers | 1 | 0 | 15-May-14 A | 19-May-14 A | |
| I-4002 | East Stitched - Install framing and windows | 9 | 0 | 19-May-14 A | 09-Jun-14 A | |
| I-2320 | RFI 233/ Install dampers | 1 | 0 | 20-May-14 A | 26-May-14 A | |
| L10-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L11-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L12-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| RF-4038 | AR - Concrete pads and curbs | 5 | 0 | 21-May-14 A | 04-Jun-14 A | |
| ASI27cap | ASI No. 27 - City Approved ASI No. 27 (Plumbing) | 0 | 0 | 21-May-14 A | | |
| ASI38 | ASI No. 38 - MDP's Bar & Concierge Plumbing Revisi | 0 | 0 | 22-May-14 A | | |
| L1BOH2-8124 | Flooring - VCT at Luggage Room | 2 | 0 | 22-May-14 A | 26-May-15 A | |
| L10-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L11-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L12-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L14-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L15-8221 | HVAC Risers Duct Insulation | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 27-May-14 A | |
| L11-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 07-Jun-14 A | |
| L12-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 27-May-14 A | 05-Jun-14 A | |
| L07-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 27-May-14 A | 06-Jun-14 A | |
| I-2322 | New Activity | 1 | 0 | 27-May-14 A | 28-May-14 A | |
| I-3002 | ASI 38/ City of Bellevue approve bar design changes | 5 | 0 | 28-May-14 A | 12-Dec-14 A | |
| I-4502 | Release metal panels for fabrication | 0 | 0 | 28-May-14 A | | |
| I-4504 | Metal panel fabrication (1st delivery) | 1 | 0 | 29-May-14 A | 08-Jul-14 A | |
| I-2324 | RFI 233/ Install dampers | 1 | 0 | 29-May-14 A | 08-Jun-14 A | |
| L16-8221 | HVAC Risers Duct Insulation | 1 | 0 | 30-May-14 A | 30-May-14 A | |

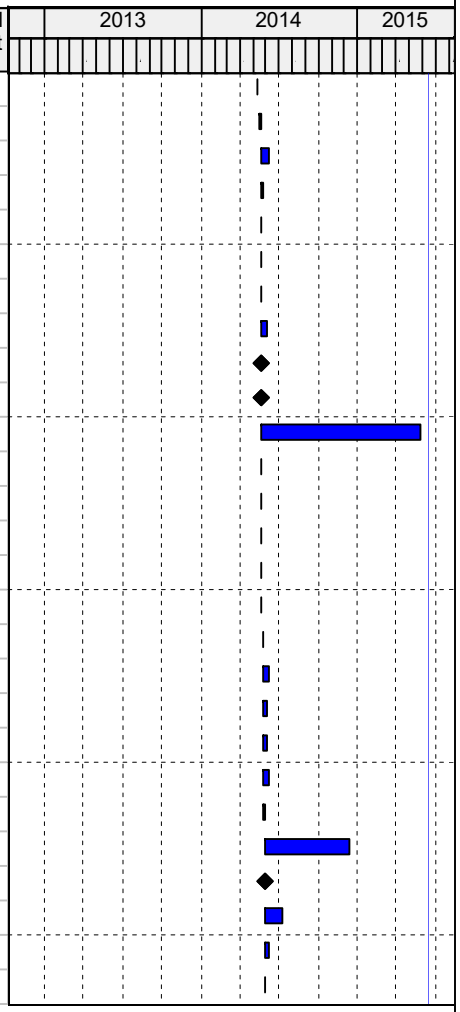


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-8712 | PH - Complete Framing and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| PH-8714 | Stage PH/L18 roofing materials | 2 | 0 | 30-May-14 A | 30-May-14 A | |
| L08-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L08-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 02-Jun-14 A | 20-Jun-14 A | |
| PH-8704I | Correct support steel embeds | 2 | 0 | 02-Jun-14 A | 11-Jun-14 A | |
| L14-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 03-Jun-14 A | 04-Jun-14 A | |
| L17-8221 | HVAC Risers Duct Insulation | 1 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| PC-4010 | PC - Fireproof Entry Roof Steel | 5 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| I-4100 | Owner resolve trap primers issue (RFI 560) | 5 | 0 | 03-Jun-14 A | 20-Jun-14 A | |
| RF-6028 | Tower Roof - Structural Steel | 5 | 0 | 04-Jun-14 A | 17-Jun-14 A | |
| L14-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L15-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L16-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 05-Jun-14 A | 05-Jun-14 A | |
| L1B-6005 | Head of Wall Fire Caulk at CMU (including East Servic | 2 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| ASI36r1 | ASI No. 36 (Revised) - MDP's Revision to E002 | 0 | 0 | 05-Jun-14 A | | |
| L14-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L15-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| L16-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 06-Jun-14 A | 06-Jun-14 A | |
| ASI39 | ASI No. 39 - MDP's Electrical Revisions Rev. 17 | 0 | 0 | 09-Jun-14 A | | |
| I-2326 | RFI 233/ Install dampers | 1 | 0 | 09-Jun-14 A | 09-Jun-14 A | |
| I-2328 | RFI 233/ Install dampers | 1 | 0 | 09-Jun-14 A | 09-Jun-14 A | |
| I-2330 | RFI 233/ Install dampers | 1 | 0 | 10-Jun-14 A | 10-Jun-14 A | |
| L09-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 11-Jun-14 A | 12-Jun-14 A | |
| ASI25r2 | ASI No. 25 (Revised) - JBA's Interior Elevation Revisic | 0 | 0 | 11-Jun-14 A | | |
| ASI29r3 | ASI No. 29 (Revised) - JBA's Interior Elevation Revs a | 0 | 0 | 11-Jun-14 A | | |

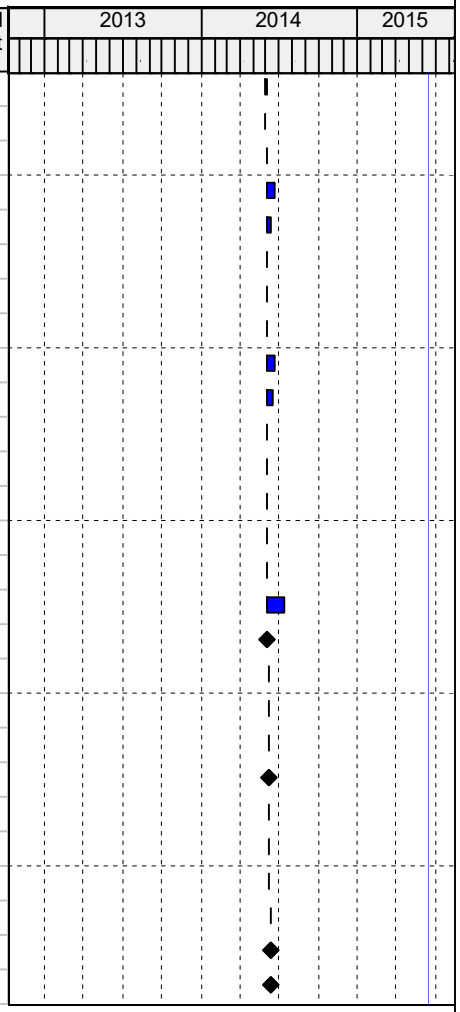


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ASI35r1 | ASI No. 35 (Revised) - JBA's Interior Design Revisions | 0 | 0 | 11-Jun-14 A | | |
| I-2332 | RFI 233/ Install dampers | 1 | 0 | 11-Jun-14 A | 12-Jun-14 A | |
| I-5018 | RFI 566 - Street Overlay Pavement Marking Reqs | 1 | 0 | 11-Jun-14 A | 01-Jul-14 A | |
| I-2970 | RFI 567 Grease Duct Conflict with Mens Restroom (P | 1 | 0 | 12-Jun-14 A | 01-Aug-14 A | |
| I-2336 | RFI 233/ Install dampers | 1 | 0 | 13-Jun-14 A | 16-Jun-14 A | |
| I-2334 | RFI 233/ Install dampers | 1 | 0 | 17-Jun-14 A | 18-Jun-14 A | |
| I-3702 | Complete wall framing at Stair/Elevator 5 (LL4) | 2 | 0 | 18-Jun-14 A | 20-Jun-14 A | |
| I-3720 | Fireproof added steel between Stair 1 and Elevator 5 | 5 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| I-3722 | Complete GWB between Stair 1 and Elevator 5 shaft | 10 | 0 | 18-Jun-14 A | 18-Jul-14 A | |
| ASI40 | ASI No. 40 - MDP's Electrical Revisions Rev. 18 | 0 | 0 | 18-Jun-14 A | | |
| LL1-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 22-Jul-14 A | |
| TC-5912 | Tower Crane pour-backs (LL4 to L3) | 4 | 0 | 19-Jun-14 A | 26-Jun-14 A | |
| LL1-Z2-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| I-2338 | RFI 233/ Install dampers | 1 | 0 | 19-Jun-14 A | 23-Jun-14 A | |
| LL4-6005 | LL4 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| LL3-6005 | LL3 - Seismic Head Of Wall Fire Caulk at CMU | 3 | 0 | 20-Jun-14 A | 18-Jul-14 A | |
| L03-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 21-Jun-14 A | 21-Jun-14 A | |
| L06-6040 | Test Heat Pumps - L3, L4, L5 and L6 | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L03-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| L17-6021 | Install Shaft Fire/Smoke Dampers & Inspect | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL2-6005 | LL2 - Seismic Head Of Wall Fire Caulk at CMU | 5 | 0 | 24-Jun-14 A | 18-Jul-14 A | |
| I-3704 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| LL1-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z2-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 14-Jul-14 A | |
| LL1-Z3-6005 | Head of Wall Fire Caulk at CMU | 2 | 0 | 24-Jun-14 A | 04-Aug-14 A | |
| L1L-6005 | Head of Wall Fire Caulk at CMU (including back of ho | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1K-6005 | Head of Wall Fire Caulk at CMU & Inspection | 2 | 0 | 24-Jun-14 A | 08-Aug-14 A | |

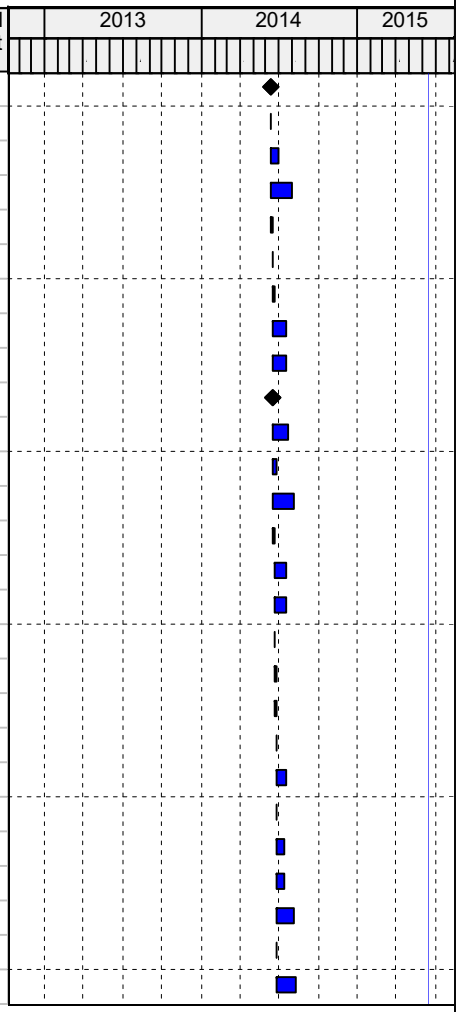



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L04-7022 | Fire Sprinkler Rough-In | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| I-2340 | RFI 233/ Install dampers | 1 | 0 | 24-Jun-14 A | 26-Jun-14 A | |
| L17-6027 | Electrical to Fire/Smoke Dampers | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| I-3710 | Complete remaining plumbing rough-in at Stair/Eleva | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| I-3712 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 25-Jun-14 A | 17-Jul-14 A | |
| L1K-6018a | Install Kitchen hoods and grease ducts (OFCI) | 10 | 0 | 25-Jun-14 A | 07-Oct-14 A | |
| L03-8604 | L3 Pool - Plumbing R/I | 5 | 0 | 25-Jun-14 A | 10-Nov-14 A | |
| ASI41 | ASI No. 41 - Kay Lang's Interior Design CD Set | 0 | 0 | 25-Jun-14 A | | |
| L04-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 26-Jun-14 A | 03-Jul-14 A | |
| L09-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 26-Jun-14 A | 26-Jun-14 A | |
| I-3706 | Complete remaining HVAC rough-in at Stair/Elevator | 5 | 0 | 26-Jun-14 A | 10-Jul-14 A | |
| L03-8600 | L3 Pool - Framing & HM frames | 5 | 0 | 26-Jun-14 A | 20-Nov-14 A | |
| L05-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L08-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L04-7018 | Electrical Rough-In | 1 | 0 | 27-Jun-14 A | 22-Jul-14 A | |
| L04-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 27-Jun-14 A | 23-Jul-14 A | |
| I-2342 | RFI 233/ Install dampers | 1 | 0 | 27-Jun-14 A | 28-Jun-14 A | |
| L03-7020 | HVAC Rough-In | 1 | 0 | 29-Jun-14 A | 15-Jul-14 A | |
| L1RR-8100 | Insulation [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8100 | Insulation [DELETED - included in Ballroom activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8100 | Insulation [DELETED - included in Meeting Rooms ac | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8102 | GWB Hang [DELETED - included in Meeting Rooms a | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8215 | GWB Tape [DELETED - included in Meeting Rooms a | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z5-8104 | Prime Paint [DELETED - included in Meeting Rooms | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |

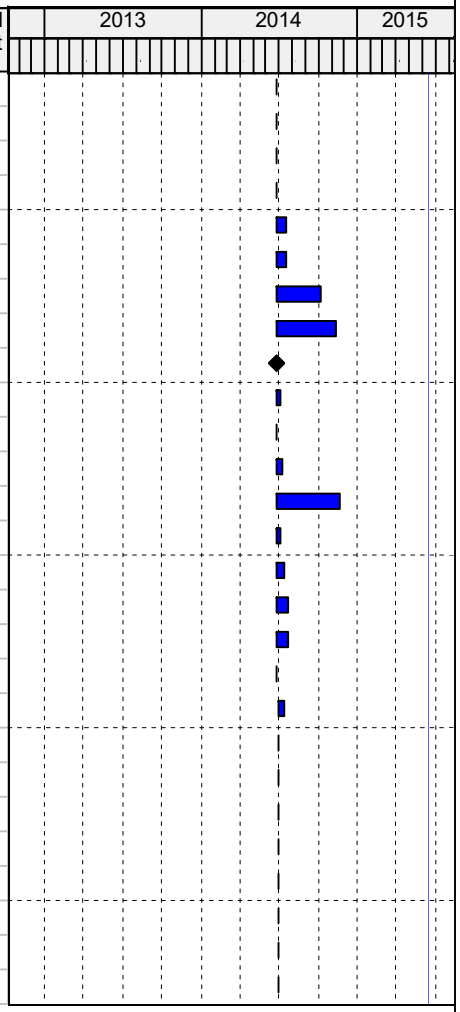


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z6-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z6-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8100 | Insulation [DELETED - included in Food Prep activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8102 | GWB Hang [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8215 | GWB Tape [DELETED - included in Food Prep activiti | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| LL1-Z7-8104 | Prime Paint [DELETED - included in Food Prep activit | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8102 | GWB Hang [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8215 | GWB Tape [DELETED - included in Ballroom activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1BOH1-8104 | Prime Paint [DELETED - included in Ballroom activitie | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8102 | GWB Hang [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8215 | GWB Tape [DELETED - included in Kitchen activities] | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1RR-8104 | Prime Paint [DELETED - included in Kitchen activities | 0 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L03-7018 | Electrical Rough-In | 1 | 0 | 01-Jul-14 A | 14-Jul-14 A | |
| L03-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Jul-14 A | 15-Jul-14 A | |
| I-5020 | RFI 583 - Tree Grate Location | 1 | 0 | 01-Jul-14 A | 23-Jul-14 A | |
| I-5022 | RFI 585 - Porte Cochere Concrete Bench & Planters | 1 | 0 | 01-Jul-14 A | 09-Jul-14 A | |
| I-5024 | RFI 586 - Bench Support at Porte Cochere (related to | 1 | 0 | 01-Jul-14 A | 09-Jul-14 A | |
| L10-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L03-7102 | Install Vertical Heat Pump | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L03-7116 | Frame Walls | 1 | 0 | 02-Jul-14 A | 14-Jul-14 A | |
| L03-7118 | Install HM Door Frame | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L04-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L05-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L06-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L07-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L08-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |

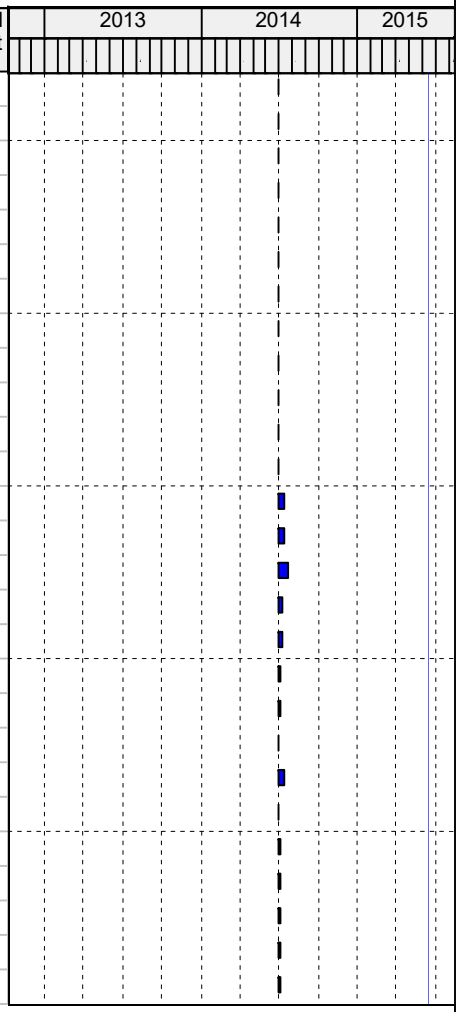


Actual Work | Critical Remai...
Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L10-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| L12-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 02-Jul-14 A | 03-Jul-14 A | |
| I-3906 | Ballroom Parapet Height Issue/ frame parapet | 1 | 0 | 02-Jul-14 A | 21-Jul-14 A | |
| L06-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| I-3708 | Complete wall framing at Stair/Elevator 5 (LL3) | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L03-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L11-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 03-Jul-14 A | 07-Jul-14 A | |
| L04-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L05-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L06-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L07-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L08-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L09-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L10-7102 | Install Vertical Heat Pump | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L17-6033 | Frame Shaft Walls & Inspect (Part 2) | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L10-6040 | Test Heat Pumps - L7, L8, L9 and L10 | 3 | 0 | 07-Jul-14 A | 09-Jul-14 A | |
| L10-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L03-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |

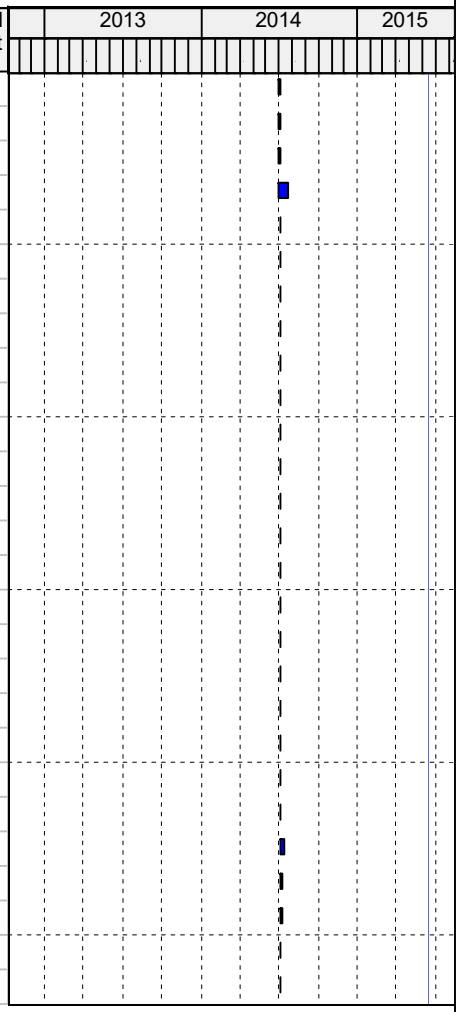



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L04-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L05-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L06-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L07-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L08-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L09-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L10-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L11-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L12-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L14-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L14-7102 | Install Vertical Heat Pump | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L11-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Jul-14 A | 29-Jul-14 A | |
| L03-8602 | L3 Pool - Fire Sprinkler R/I | 5 | 0 | 08-Jul-14 A | 22-Jul-14 A | |
| L03-7016 | Install HM door frame | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L03-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L11-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L16-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 09-Jul-14 A | |
| L04-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |

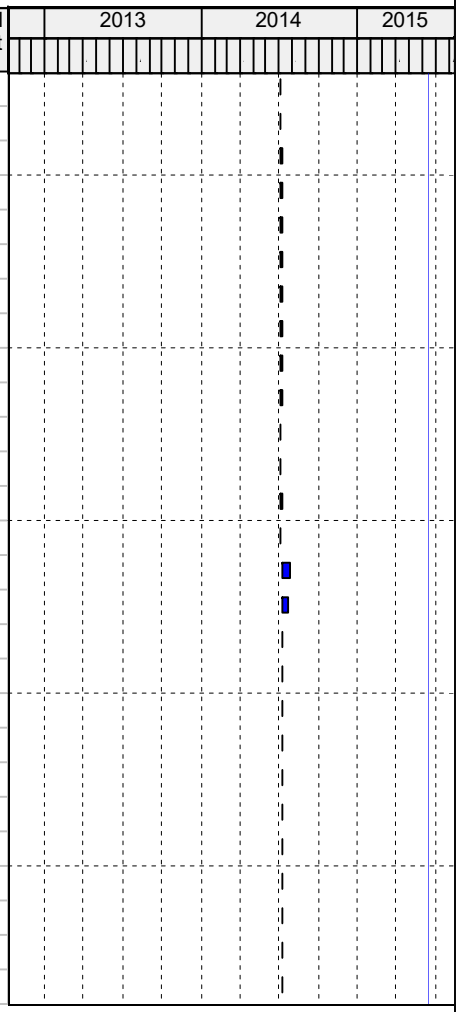



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L04-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L05-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L06-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L07-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L08-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L09-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L12-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| MP-FAB1 | Fabricate and Deliver Bronze Gold Horizontal Panels | 30 | 0 | 09-Jul-14 A | 15-Jul-14 A | |
| L04-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L05-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L06-7116 | Frame Walls | 1 | 0 | 09-Jul-14 A | 14-Jul-14 A | |
| L16-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| MP-FAB2 | Fabricate and Deliver Silver Vertical Panels | 45 | 0 | 10-Jul-14 A | 25-Aug-14 A | |

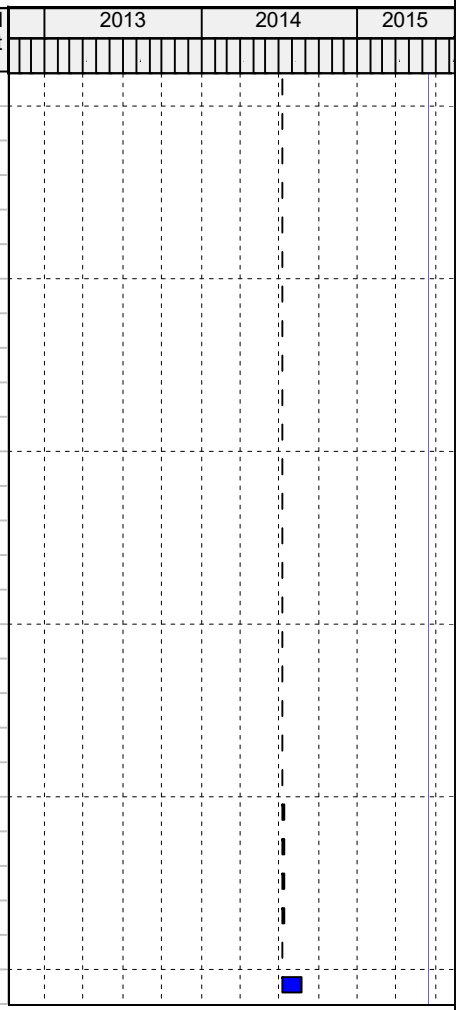



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ASI27capt | ASI No. 27 - City Approved ASI No. 27 (Tower Plumbi | 0 | 0 | 10-Jul-14 A | | |
| ASI27cam | ASI No. 27 - City Approved ASI No. 27 (Mechanical) | 0 | 0 | 10-Jul-14 A | | |
| ASI36ca | ASI No. 36 - MDP Electrical Revisions Rev. 16 (City Ap | 0 | 0 | 10-Jul-14 A | | |
| ASI38ca | ASI No. 38 - MDP's Bar & Concierge Plumbing Revisi | 0 | 0 | 10-Jul-14 A | | |
| I-5026 | RFI 611 - Landscaping at Porte Cochere Planters | 1 | 0 | 10-Jul-14 A | 18-Jul-14 A | |
| I-3004 | ASI 38/ Issue ASI 38 | 0 | 0 | 11-Jul-14 A | | |
| I-3006 | ASI 38/ Release bar area for x-ray examination | 5 | 0 | 11-Jul-14 A | 03-Sep-14 A | |
| L07-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| LL1-Z2-6018a | Complete Mech RI at tower crane opening (LL1) | 4 | 0 | 14-Jul-14 A | 17-Jul-14 A | |
| L08-6223 | Frame Corridor Ceilings | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| SW-2006a | Complete Dry Utilities (Phase 2) | 5 | 0 | 14-Jul-14 A | 24-Jul-14 A | |
| L04-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L04-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L05-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L06-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L06-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L04-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L05-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |

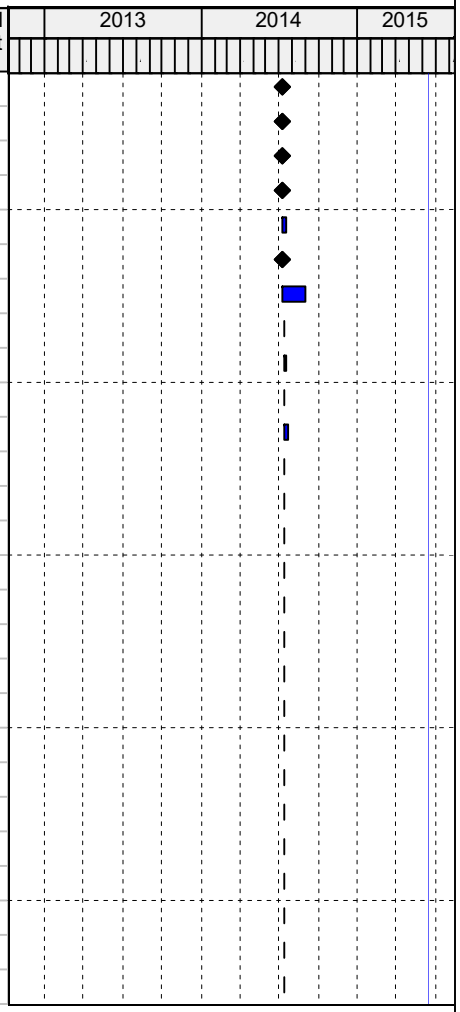



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7118 | Install HM Door Frame | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L07-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L07-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L08-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L08-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L09-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L09-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L10-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L10-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L11-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L11-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L12-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L12-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L15-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 14-Jul-14 A | 15-Jul-14 A | |
| L15-7102 | Install Vertical Heat Pump | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L1B-6026 | Install operable partition steel | 2 | 0 | 15-Jul-14 A | 08-Aug-14 A | |
| L09-6223 | Frame corridor ceilings | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L03-7120 | Electrical Rough-In | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L07-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L07-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L08-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L08-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L09-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L09-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 15-Jul-14 A | 15-Jul-14 A | |
| L03-7142 | Install Laundry Chute (All Levels) | 9 | 0 | 15-Jul-14 A | 25-Jul-14 A | |
| LL2-2045 | LL2 - Electrical Room build-out | 15 | 0 | 15-Jul-14 A | 26-Sep-14 A | |
| L03-7122 | HVAC Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |

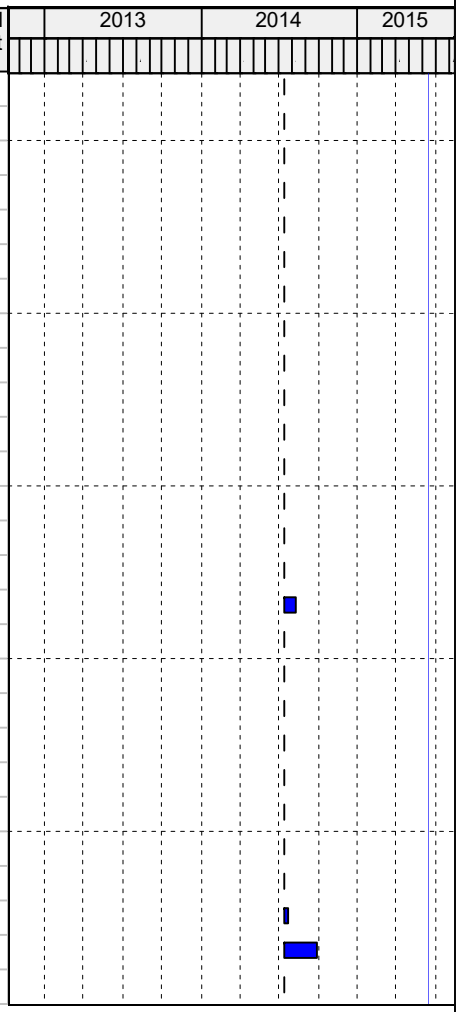


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L04-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L05-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L06-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L07-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L07-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L08-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L08-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L09-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L09-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L04-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L05-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-7124 | Fire Sprinkler Rough-In | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L10-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L10-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L11-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L11-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L12-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L12-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L15-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L15-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |

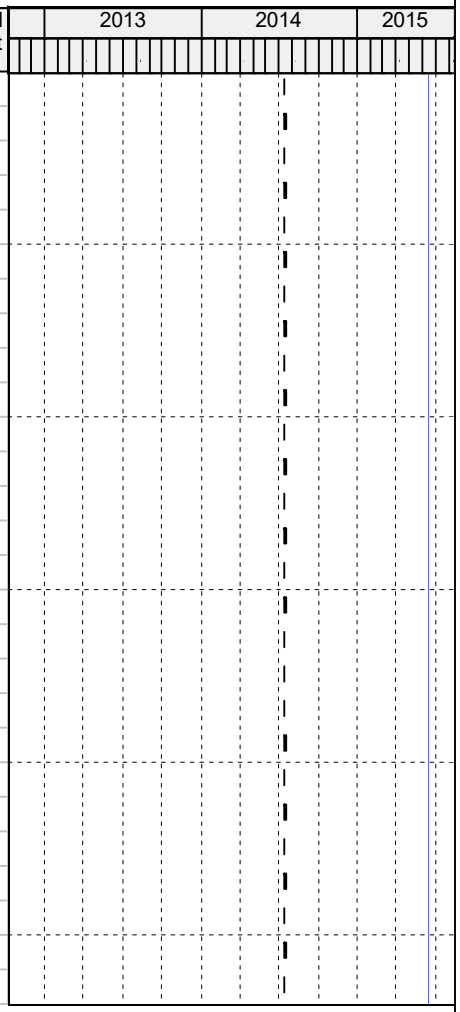



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L17-7100 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 16-Jul-14 A | 17-Jul-14 A | |
| L17-7102 | Install Vertical Heat Pump | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| ASI41r1 | ASI No. 41 (Revised) - Kay Lang's Interior Design CD | 0 | 0 | 16-Jul-14 A | | |
| ASI43 | ASI No. 43 - MDP's Electrical Revisions Rev. 19 | 0 | 0 | 16-Jul-14 A | | |
| L03-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L04-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L04-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L05-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L05-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L06-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L06-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L07-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L08-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L09-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L07-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L08-7118 | Install HM Door Frame | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L09-7116 | Frame Walls | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L10-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L10-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |

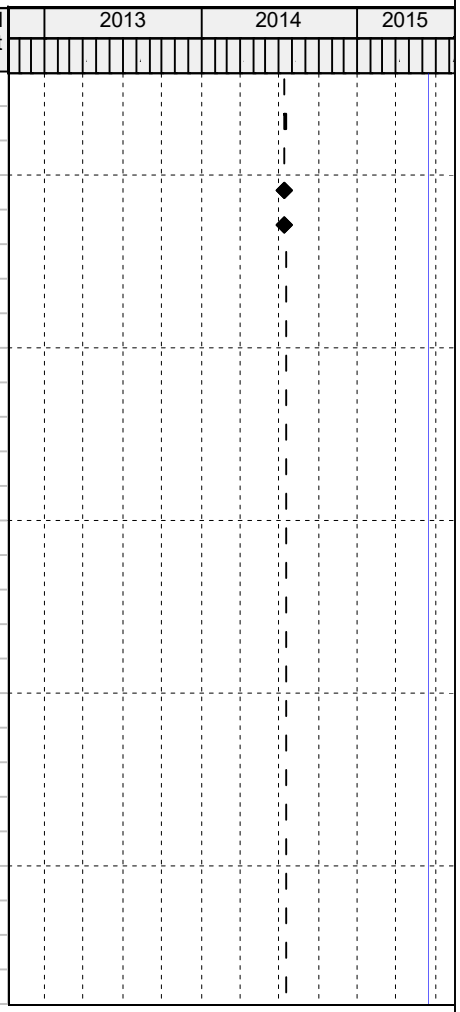



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L11-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L12-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L12-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 17-Jul-14 A | 18-Jul-14 A | |
| L16-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| ASI42 | ASI No. 42 - JBA's Arch Revs to Lobby and Concierge | 0 | 0 | 17-Jul-14 A | | |
| ASI45 | ASI No. 45 - JBA's Revised Guestroom Suite Layouts | 0 | 0 | 17-Jul-14 A | | |
| L03-8608 | L3 Pool - Electrical R/I | 5 | 0 | 18-Jul-14 A | 10-Nov-14 A | |
| L03-8610 | L3 Pool - Fire Alarm / Elec Specialties R/I | 5 | 0 | 18-Jul-14 A | 10-Nov-14 A | |
| L15-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L15-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| L17-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Jul-14 A | 21-Jul-14 A | |
| L17-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Jul-14 A | 18-Jul-14 A | |
| LL2-2052 | LL2 - Install fuel piping and exhaust duct to Generatc | 8 | 0 | 21-Jul-14 A | 15-Aug-14 A | |
| L04-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L04-7016 | Install HM door frame | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L07-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L08-7124 | Fire Sprinkler Rough-In | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L10-7116 | Frame Walls | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L16-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 21-Jul-14 A | 22-Jul-14 A | |
| L16-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| L17-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| ASI41r2 | ASI No. 41 (Revised) - Kay Lang's Interior Design Spe | 0 | 0 | 22-Jul-14 A | | |
| ASI44 | ASI No. 44 - MDP's Mechanical Revisions Rev. 17 | 0 | 0 | 24-Jul-14 A | | |
| MPT-1002 | Tower - Install Elevation 35 (east elevation-south half) | 8 | 0 | 25-Jul-14 A | 04-Aug-14 A | |
| L16-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 25-Jul-14 A | 25-Jul-14 A | |

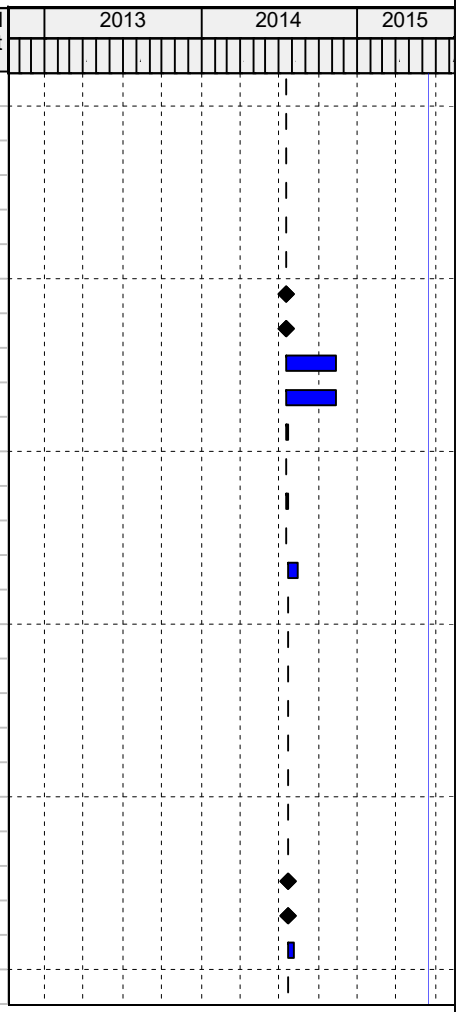


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L14-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 28-Jul-14 A | 28-Jul-14 A | |
| L15-7000 | HVAC Riser/Damper - Install & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L16-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L10-6223 | Frame Corridor Ceilings | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L11-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L15-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L15-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 29-Jul-14 A | 29-Jul-14 A | |
| L11-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L12-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L14-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L16-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| I-1304 | Prep Kitchen - Additional framing (ASI 30) | 2 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-2302 | Framing "Go Back" work at LL1 for RFI 233 | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| I-2502 | Electrical rework at LL1 for ASIs 7, 9r2, 14, 27 | 4 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| L12-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L1B-6016I | A/V vendor & equipment (EQUIPMENT BY OTHERS, | 10 | 0 | 01-Aug-14 A | 15-Aug-14 A | |
| MPL4-1000 | Upper L4 Ballroom - Install Elevations 1, 2 & 3 (south | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1000 | Tower - Install Elevations 26-27 (west elevation) [DEL | 13 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPP-1002 | Podium - Install Elevations 1 & 2 (west elevation, sou | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPP-1008 | Podium - Install Elevations 7 & 8 (north & east elevati | 9 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPL4-1002 | Upper L4 Ballroom - Install Elevation 10 (west elevatic | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |

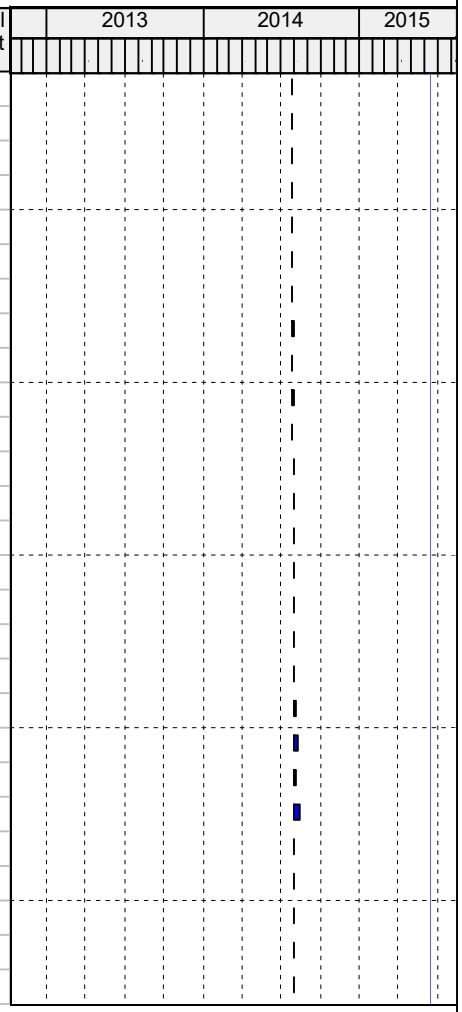



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPL4-1004 | Upper L4 Ballroom - Install Elevation 9 (north elevatio | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1006 | Tower - Install Elevation 40 (east return-east end) [DE | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| MPT-1010 | Tower - Install Elevations 51 (north elevation) [DELET | 8 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| I-4004 | East Stitched - Install metal panels [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L09-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L10-7016 | Install HM door frame | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L11-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L11-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L15-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L14-7106 | HVAC Firestop & Inspect (1) | 1 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| L17-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| MPT-1010b | Tower - Install Elevation 45 [DELETED] | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| ASI46 | ASI No. 46 - Concept Services Revised Kitchen Drawi | 0 | 0 | 01-Aug-14 A | | |
| L16-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 04-Aug-14 A | 05-Aug-14 A | |
| L11-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Aug-14 A | 08-Aug-14 A | |
| L04-7020 | HVAC Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L05-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L06-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L07-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |

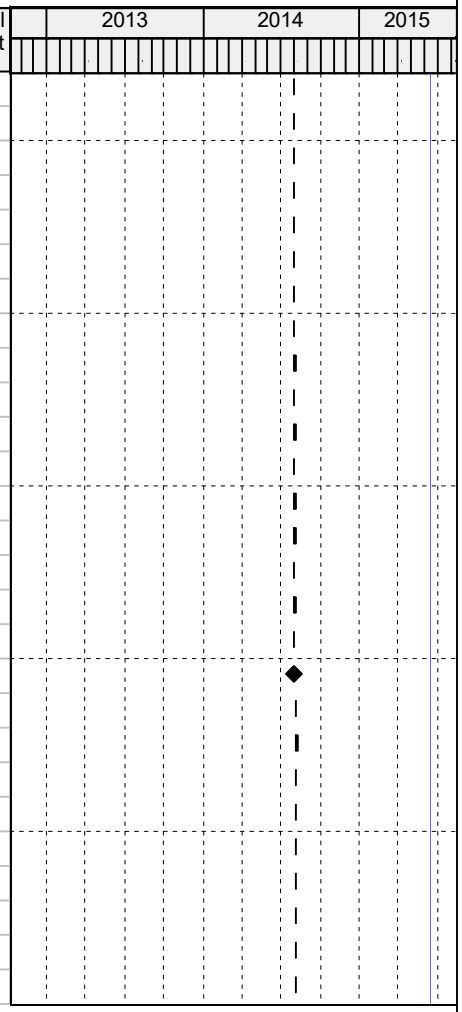



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L08-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L09-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7018 | Electrical Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L10-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L14-7104 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L15-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 05-Aug-14 A | 07-Aug-14 A | |
| L05-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L06-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L07-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L08-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L09-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L10-7020 | HVAC Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7018 | Electrical Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L11-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| L14-7108 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 05-Aug-14 A | 06-Aug-14 A | |
| L14-7110 | HVAC Firestop & Inspect (2) | 1 | 0 | 05-Aug-14 A | 05-Aug-14 A | |
| I-4104 | Install added trap primers - LL1 | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L06-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L07-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L08-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L09-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L10-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L11-7020 | HVAC Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |

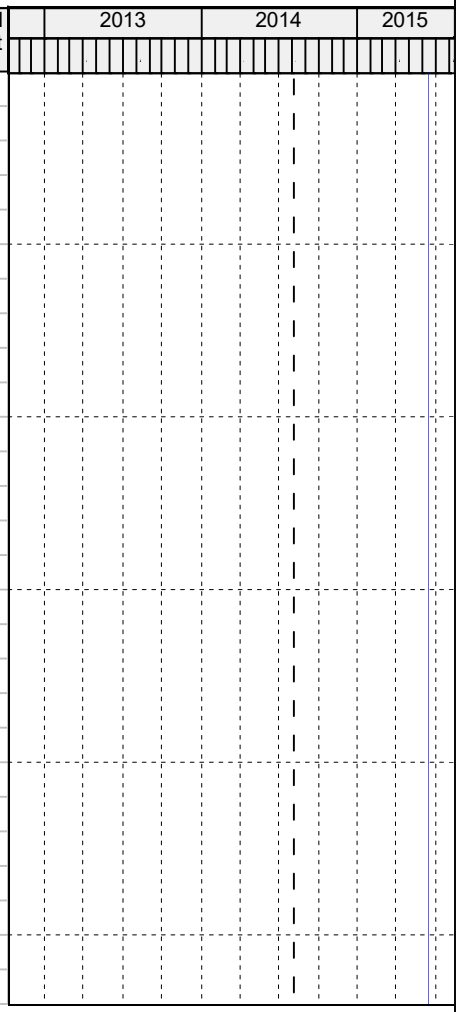



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7022 | Fire Sprinkler Rough-In | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L14-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L16-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L16-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| EL-1220 | Elevator fronts delivered | 0 | 0 | 07-Aug-14 A | | |
| L12-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L12-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-6223 | Frame Corridor Ceilings | 4 | 0 | 08-Aug-14 A | 12-Aug-14 A | |
| L11-7016 | Install HM door frame | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L12-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L12-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L14-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L14-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L15-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L15-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L16-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L16-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| L17-7112 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| L17-7114 | HVAC Firestop & Inspect (3) | 1 | 0 | 08-Aug-14 A | 08-Aug-14 A | |
| ASI48 | ASI No. 48 - MDP Revisions to Electrical & Plumbing | 0 | 0 | 08-Aug-14 A | | |
| L14-6040 | Test Heat Pumps - L11, L12 and L14 | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| PH-6026 | PH - Insulation/Vapor Barrier/GWB at Exterior Walls | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| L11-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |

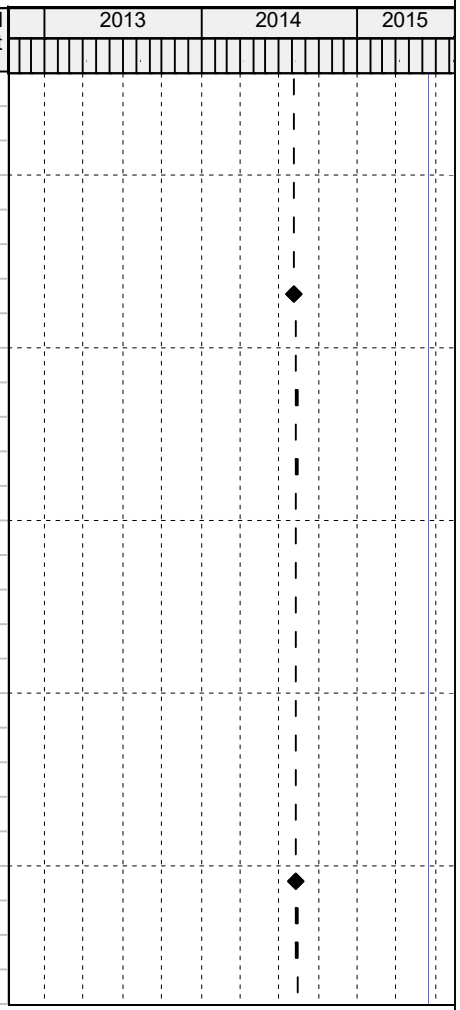


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-7026 | Inspections for GWB Cover | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L12-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L15-7016 | Install HM door frame | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L14-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 13-Aug-14 A | 13-Aug-14 A | |
| L15-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 14-Aug-14 A | 15-Aug-14 A | |
| LL2E-8108 | LL2 - Set fire pumps and equipment | 5 | 0 | 14-Aug-14 A | 29-Sep-14 A | |
| L10-7028 | GWB Hang/Tape/Finish | 5 | 0 | 14-Aug-14 A | 05-Dec-14 A | |
| L12-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L12-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L14-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L15-7022 | Fire Sprinkler Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L16-7020 | HVAC Rough-In | 1 | 0 | 14-Aug-14 A | 14-Aug-14 A | |
| L1BOH2-6008 | Int Wall Framing & Inspection | 5 | 0 | 14-Aug-14 A | 20-Aug-14 A | |
| I-4106 | Install added trap primers - L1 | 1 | 0 | 15-Aug-14 A | 15-Aug-14 A | |
| L14-6223 | Frame Corridor Ceilings | 4 | 0 | 15-Aug-14 A | 16-Aug-14 A | |
| L03-8136 | Install Counter Subtops | 3 | 0 | 15-Aug-14 A | 18-Aug-14 A | |
| LL2-2054 | LL2 - GWB, Hang 1st Layer at Laundry Room | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| LL2E-8112 | LL2 - Form/Pour Fire Pump Pads/Curbs | 2 | 0 | 16-Aug-14 A | 18-Aug-14 A | |
| LL1-6014Ia | L1 bar redesign - rework plumbing at ceilings | 10 | 0 | 18-Aug-14 A | 05-Jan-15 A | |
| L15-6223 | Frame Corridor Ceilings | 4 | 0 | 18-Aug-14 A | 21-Aug-14 A | |

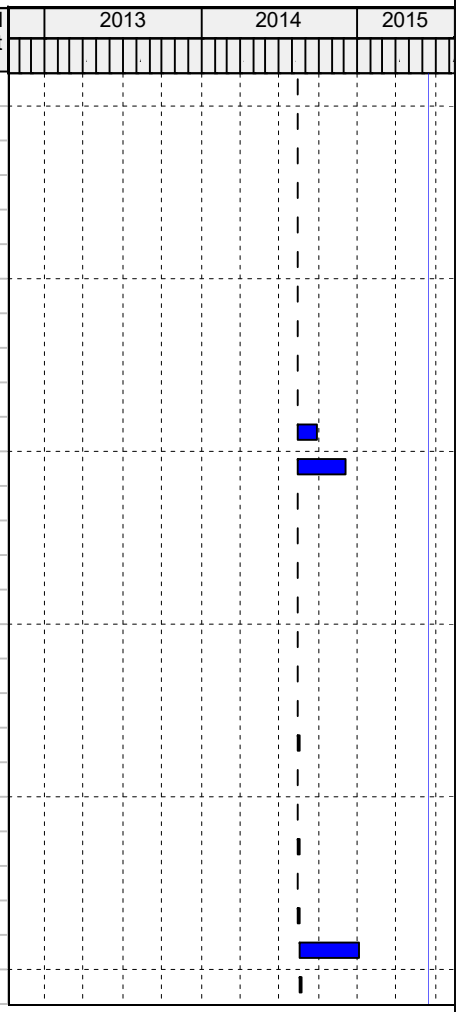


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7002 | Frame Shaft Wall/Core Board/Firestop & Inspect | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-7004 | HVAC Firestop & Inspect (1) | 1 | 0 | 18-Aug-14 A | 18-Aug-14 A | |
| L04-8136 | Install Counter Subtops | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-6014Ic | L1 bar redesign - rework electrical at ceilings | 10 | 0 | 18-Aug-14 A | 05-Jan-15 A | |
| LL2E-8114 | LL2 - Set Tube Steel at Door | 1 | 0 | 19-Aug-14 A | 19-Aug-14 A | |
| L17-7006 | Pre-Rock Shafts 1st Layer & Inspect | 2 | 0 | 20-Aug-14 A | 21-Aug-14 A | |
| L17-7008 | HVAC Firestop & Inspect (2) | 1 | 0 | 20-Aug-14 A | 20-Aug-14 A | |
| L05-8136 | Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 26-Aug-14 A | |
| L06-8136 | Bathrooms - Install Counter Subtops | 3 | 0 | 20-Aug-14 A | 13-Oct-14 A | |
| L16-6223 | Frame Corridor Ceilings | 4 | 0 | 21-Aug-14 A | 29-Aug-14 A | |
| L17-7010 | Pre-Rock Shafts 2nd Layer & Inspect | 2 | 0 | 21-Aug-14 A | 22-Aug-14 A | |
| L17-7012 | HVAC Firestop & Inspect (3) | 1 | 0 | 21-Aug-14 A | 21-Aug-14 A | |
| L1BOH2-6016 | Electrical RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 21-Aug-14 A | 02-Oct-14 A | |
| L1BOH2-6018 | HVAC RI | 4 | 0 | 21-Aug-14 A | 17-Oct-14 A | |
| L15-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7020 | HVAC Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L17-7022 | Fire Sprinkler Rough-In | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| LL2E-8116 | LL2 - Set Door Jamb | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| ASI49 | ASI No. 49 - SCA Transformer Vault Alcove Connectic | 0 | 0 | 22-Aug-14 A | | |
| L03-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-8201 | Install ACT Grid @ Corridors | 2 | 0 | 25-Aug-14 A | 26-Aug-14 A | |
| L04-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L04-7028 | GWB Hang/Tape/Finish | 5 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L05-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L05-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L06-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |

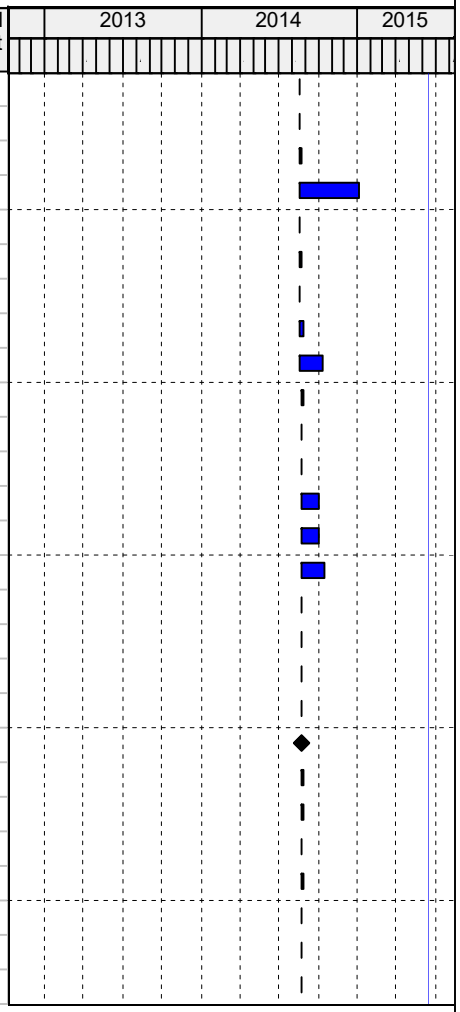



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L07-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L08-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7026 | Inspections for GWB Cover | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7018 | Electrical Rough-In | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7014 | Frame Wall & Soffit (x41/x42) | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L17-7016 | Install HM door frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L11-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L12-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L14-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L15-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7116 | Frame Walls | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L16-7118 | Install HM Door Frame | 1 | 0 | 25-Aug-14 A | 25-Aug-14 A | |
| L03-8123 | Bathroom "Barn Doors" On Site | 0 | 0 | 25-Aug-14 A | | |
| LL3-6026 | LL3 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL2-6026 | LL2 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| LL1-Z3-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L1BOH2-6026 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |

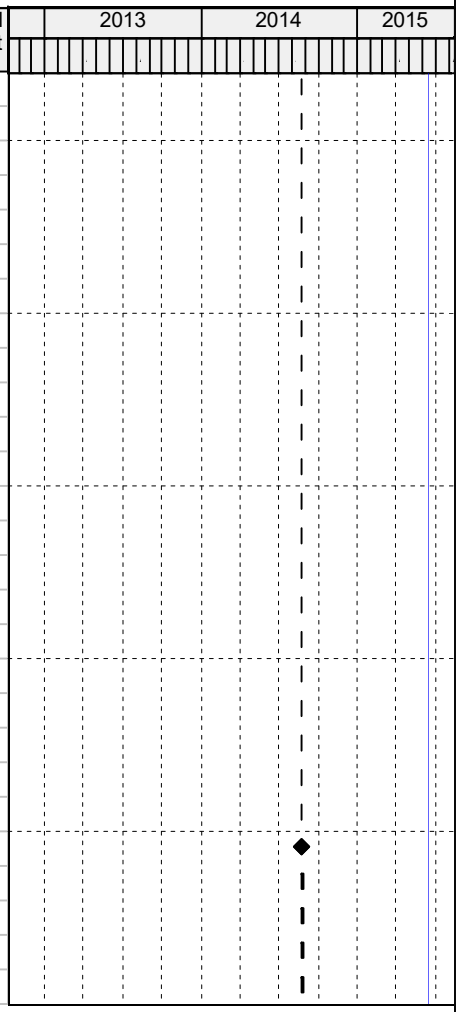



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-6026 | L2 - Set Elevator Fronts (Cars 1-4 | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L03-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L04-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L05-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L06-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L07-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L08-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L09-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L10-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L11-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L12-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 27-Aug-14 A | |
| L14-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L15-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 28-Aug-14 A | |
| L16-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| L17-8397 | Set Elevator Fronts (Cars 1-4) | 1 | 0 | 25-Aug-14 A | 29-Aug-14 A | |
| MPT-1008 | Tower - Install E/W Wing, N. Side West Half (Elev 50,: | 7 | 0 | 26-Aug-14 A | 03-Oct-14 A | |
| L06-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L07-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L08-6005 | CMU Fire Caulk/Clips | 2 | 0 | 26-Aug-14 A | 01-Nov-14 A | |
| L05-7026 | Inspections for GWB Cover | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L05-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L11-7028 | GWB Hang/Tape/Finish | 5 | 0 | 26-Aug-14 A | 08-Dec-14 A | |
| L12-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L14-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L03-8105a | Painting - Split Door Jambs | 1 | 0 | 26-Aug-14 A | 26-Aug-14 A | |
| L09-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L10-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |

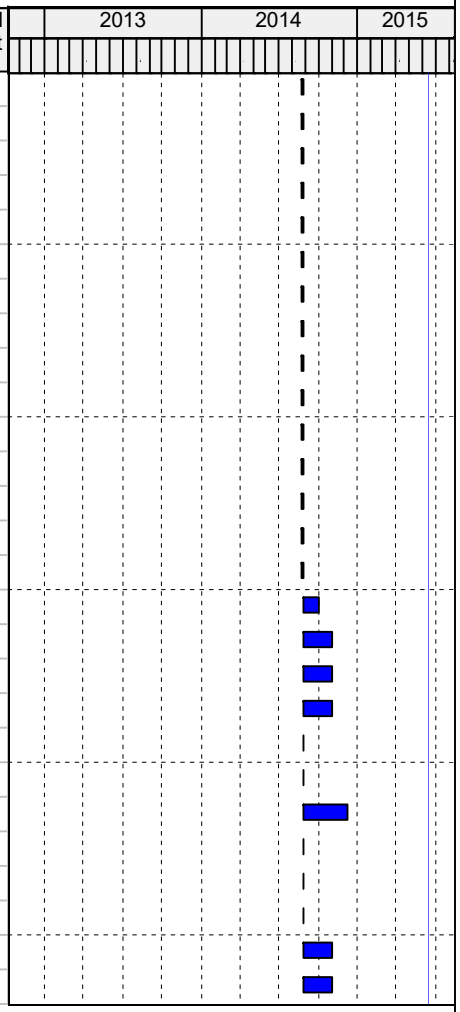


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L12-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L14-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L15-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L16-6005 | CMU Fire Caulk/Clips | 2 | 0 | 27-Aug-14 A | 01-Nov-14 A | |
| L05-8201 | Install ACT Grid @ Corridors | 2 | 0 | 27-Aug-14 A | 28-Aug-14 A | |
| L16-7022 | Fire Sprinkler Rough-In | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L04-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| L06-8105a | Painting - Split Door Jambs | 1 | 0 | 27-Aug-14 A | 27-Aug-14 A | |
| EP-5110a | L1 - Install Steel at Revolving Door Opening | 3 | 0 | 27-Aug-14 A | 29-Aug-14 A | |
| L05-8105a | Painting - Split Door Jambs | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| ASI50 | ASI No. 50 - Updated S1 Plumbing Fixture | 0 | 0 | 28-Aug-14 A | | |
| I-4102 | Install added trap primers - LL2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4108 | Install added trap primers - L2 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4110 | Install added trap primers - L3 | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| I-4112 | Install added trap primers - Roof PH | 1 | 0 | 29-Aug-14 A | 29-Aug-14 A | |
| L03-8124d | Flooring On Site and Acclimated | 2 | 0 | 29-Aug-14 A | 01-Sep-14 A | |
| ASI47 | ASI No. 47 - Architectural and Interior Design Revisior | 0 | 0 | 29-Aug-14 A | | |
| L02-5102 | L2 - Storefront Frames | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| L04-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L05-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L17-6005 | CMU Fire Caulk/Clips | 2 | 0 | 02-Sep-14 A | 01-Nov-14 A | |
| L03-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L12-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L14-7026 | Inspections for GWB Cover | 1 | 0 | 02-Sep-14 A | 02-Sep-14 A | |
| L07-8136 | Install Counter Subtops | 3 | 0 | 02-Sep-14 A | 04-Sep-14 A | |
| LL1-Z3-FCC10 | FCC - Set Jamb | 1 | 0 | 02-Sep-14 A | 03-Sep-14 A | |

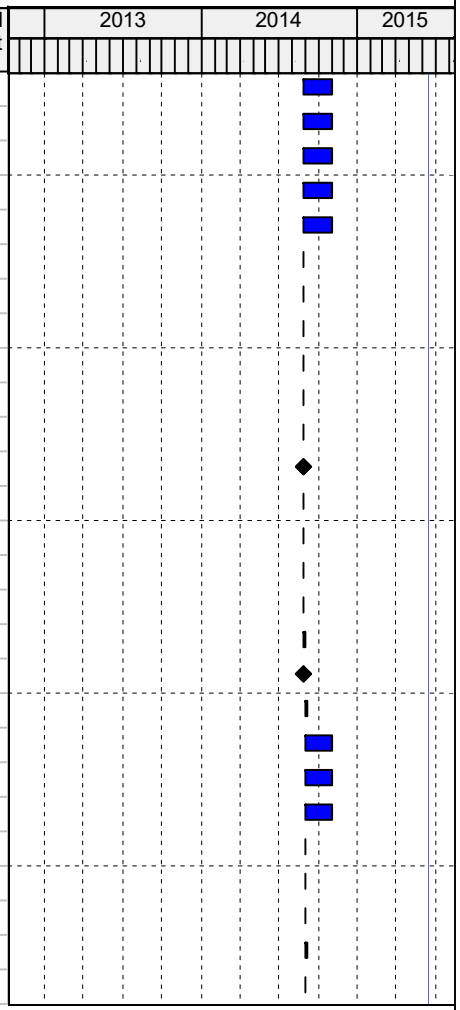



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPT-1004 | Tower - Install E/W Wing, S. Side w/o Windows (Elev | 10 | 0 | 03-Sep-14 A | 17-Oct-14 A | |
| L03-7028 | GWB Hang/Tape/Finish | 5 | 0 | 03-Sep-14 A | 02-Dec-14 A | |
| L12-7028 | GWB Hang/Tape/Finish | 5 | 0 | 03-Sep-14 A | 08-Dec-14 A | |
| L03-8126a | Doors & Hardware On Site | 0 | 0 | 03-Sep-14 A | | |
| LL1-Z3-FCC12 | FCC - Sheetrock Outside Wall | 1 | 0 | 03-Sep-14 A | 03-Sep-14 A | |
| ASI46r1 | ASI No. 46 (Revised) - Revised Kitchen Equipment M | 0 | 0 | 03-Sep-14 A | | |
| L16-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| L17-6223 | Frame Corridor Ceilings | 4 | 0 | 04-Sep-14 A | 11-Sep-14 A | |
| L02-5104b | L2 - Install Storefront Temporary Enclosures | 1 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| LL1-Z3-FCC14 | FCC - Verify Fire Caulk OK & Inspect Room OK to 2n( | 1 | 0 | 04-Sep-14 A | 04-Sep-14 A | |
| I-3008 | ASI 38/ Coordinate and perform x-ray examination | 7 | 0 | 04-Sep-14 A | 24-Sep-14 A | |
| L02-5104a | L2 - Measure/Fabricate Storefront Glazing | 15 | 0 | 05-Sep-14 A | 18-Sep-14 A | |
| LL1-Z3-FCC16 | FCC - GWB, Hang 2nd Layer | 2 | 0 | 05-Sep-14 A | 08-Sep-14 A | |
| ASI52 | ASI No. 52 - MDP Electrical Revisions Rev. 21 | 0 | 0 | 05-Sep-14 A | | |
| I-5028 | RFI 687 - Planter at Porte Cochere Grid V & 25 | 1 | 0 | 05-Sep-14 A | 10-Sep-14 A | |
| L03-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8395 | Framing at Elevator Lobby | 3 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L15-7018 | Electrical Rough-In | 1 | 0 | 08-Sep-14 A | 08-Sep-14 A | |
| EL-1228 | Construct/Approve elevator lobby framing mockup (L | 3 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| LL2E-8118 | LL2 - Frame Infill, Install Densglass & Inspect at Fire I | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L06-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L08-7026 | Inspections for GWB Cover | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L15-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7018 | Electrical Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L16-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L3-5104a | L3 - Measure/Fabricate Storefront Glazing | 15 | 0 | 09-Sep-14 A | 30-Sep-14 A | |

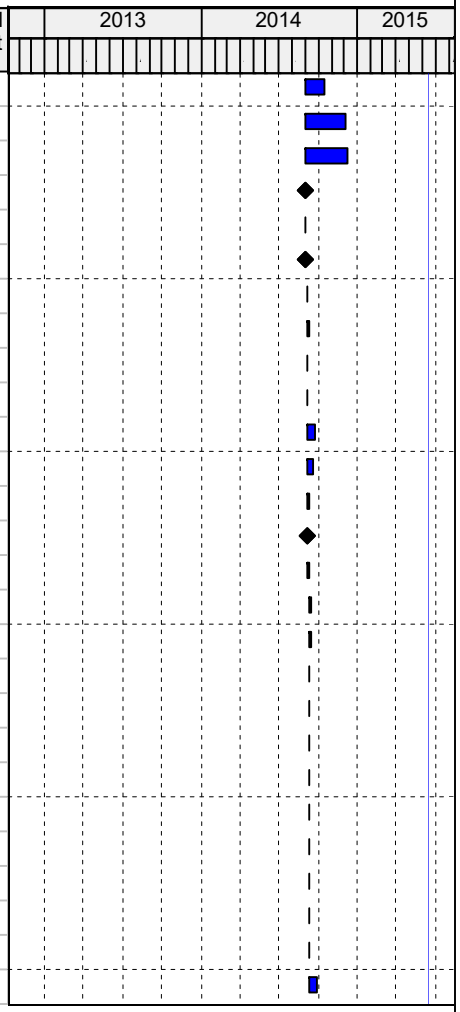



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 23-Sep-14 A | |
| L03-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L04-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| L06-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| L08-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 2 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| L05-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L06-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8395 | Framing at Elevator Lobby | 4 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L06-7028 | GWB Hang/Tape/Finish | 5 | 0 | 10-Sep-14 A | 02-Dec-14 A | |
| L08-7028 | GWB Hang/Tape/Finish | 5 | 0 | 10-Sep-14 A | 05-Dec-14 A | |
| L15-7026 | Inspections for GWB Cover | 1 | 0 | 10-Sep-14 A | 10-Sep-14 A | |
| LL2E-8120 | LL2 - Insulation, Vapor Barrier & Inspect at Fire Pump | 2 | 0 | 10-Sep-14 A | 11-Sep-14 A | |
| ASI53 | ASI No. 53 - Pool Chemical Storage System | 0 | 0 | 10-Sep-14 A | | |
| L08-8395 | Framing at Elevator Lobby | 4 | 0 | 11-Sep-14 A | 17-Sep-14 A | |
| L15-7028 | GWB Hang/Tape/Finish | 5 | 0 | 11-Sep-14 A | 08-Dec-14 A | |
| L08-8136 | Install Counter Subtops | 3 | 0 | 11-Sep-14 A | 16-Sep-14 A | |
| L02-6025 | L2 - Framing Go-Back Work (left out for mechanical e | 4 | 0 | 11-Sep-14 A | 02-Oct-14 A | |
| L1-5104a | L1 - Measure/Fabricate Storefront Glazing | 15 | 0 | 12-Sep-14 A | 18-Sep-14 A | |
| L1B-8102c | Finish framing and MEP at Main Ballroom East Wall ( | 10 | 0 | 12-Sep-14 A | 02-Oct-14 A | |
| L09-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L10-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L11-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L12-8395 | Framing at Elevator Lobby | 4 | 0 | 15-Sep-14 A | 17-Sep-14 A | |
| L16-7026 | Inspections for GWB Cover | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| MPT-1014 | Tower - Install E/W Wing, N. Side, E. Half (Elev 46-49 | 8 | 0 | 15-Sep-14 A | 28-Oct-14 A | |
| LL2-6032 | LL2 - Complete Framing (Including Elevator Lobby) | 4 | 0 | 15-Sep-14 A | 18-Sep-14 A | |
| L1-5104b | L1 - Install Storefront Temporary Enclosures | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |

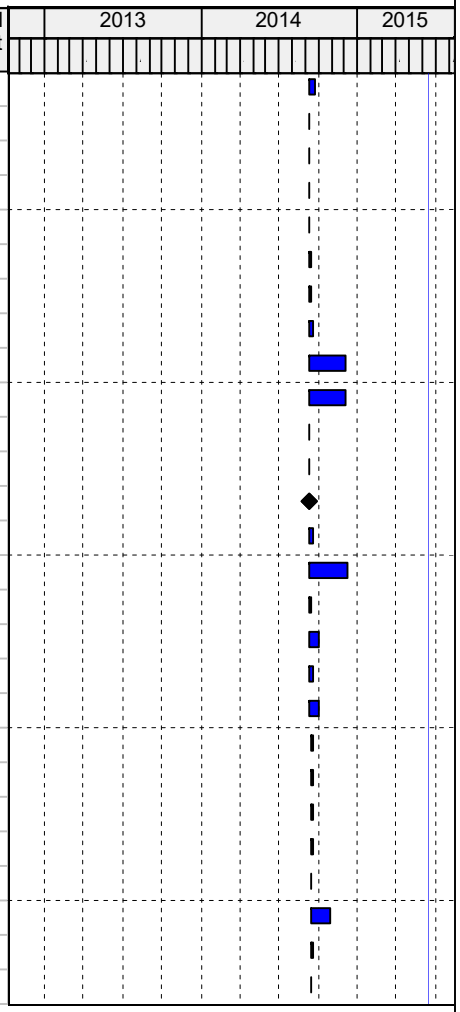



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-FCC18 | FCC - Install Temp Door | 1 | 0 | 15-Sep-14 A | 15-Sep-14 A | |
| LL2-2058a | LL2 - GWB Hang 1st Layer | 5 | 0 | 15-Sep-14 A | 19-Sep-14 A | |
| LL2-2064 | LL2 - Generator Room - Finish Exhaust Piping | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| I-3010 | ASI 38/ Prepare proposal for MEP relocations | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| ASI51 | ASI No. 51 - Interior Design Revisions | 0 | 0 | 15-Sep-14 A | | |
| L16-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L07-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L09-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L10-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| L14-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L15-8395 | Framing at Elevator Lobby | 4 | 0 | 16-Sep-14 A | 18-Sep-14 A | |
| L03-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| L16-7028 | GWB Hang/Tape/Finish | 5 | 0 | 16-Sep-14 A | 08-Dec-14 A | |
| L17-7018 | Electrical Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-7024 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L09-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L10-7118 | Install HM Door Frame | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| LL3-6028 | LL3 - Frame Elevator Lobby | 2 | 0 | 16-Sep-14 A | 17-Sep-14 A | |
| LL4-6026 | LL4 - Set Elevator Fronts (Cars 1-4) | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| I-3012 | ASI 38/ Owner approve proposal for MEP relocations | 3 | 0 | 16-Sep-14 A | 19-Sep-14 A | |
| ASI50r1 | ASI No. 50 (Revised) - Updated Plumbing Fixtgure K' | 0 | 0 | 16-Sep-14 A | | |
| L11-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L12-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L14-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L15-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L04-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L17-7026 | Inspections for GWB Cover | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |

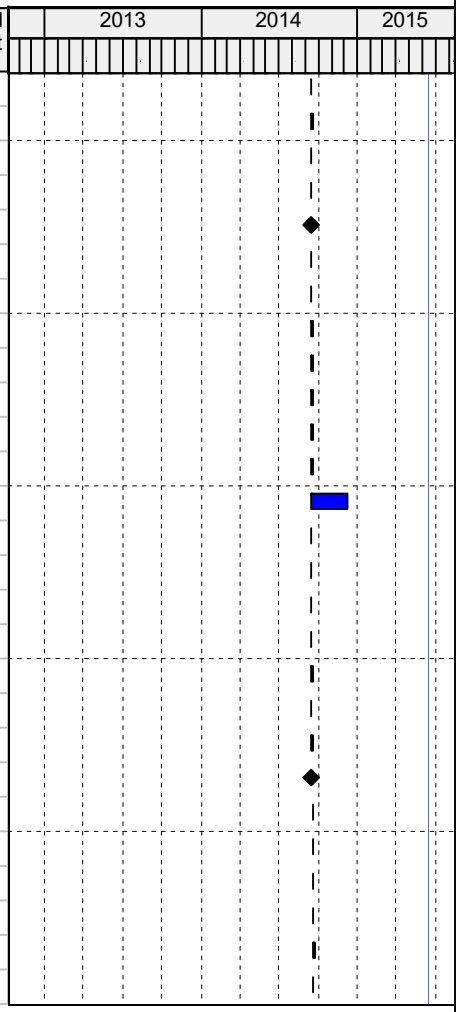



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-7116 | Frame Walls | 4 | 0 | 17-Sep-14 A | 29-Sep-14 A | |
| LL2-2066 | LL2 - Generator Room - Finish Fuel Piping | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L16-8395 | Framing at Elevator Lobby | 4 | 0 | 18-Sep-14 A | 26-Sep-14 A | |
| L02-5104 | L2 - Storefront Glazing | 2 | 0 | 18-Sep-14 A | 22-Sep-14 A | |
| L17-7028 | GWB Hang/Tape/Finish | 5 | 0 | 18-Sep-14 A | 08-Dec-14 A | |
| LL4-6028 | LL4 - Frame Elevator Lobby | 2 | 0 | 18-Sep-14 A | 02-Oct-14 A | |
| MPT-1010a | Tower - Install E/W Wing, West End (Elev 52,53) | 8 | 0 | 18-Sep-14 A | 10-Oct-14 A | |
| ASI44ca | ASI No. 44 - MDP's Mechanical Revisions Rev. 17 (Ci | 0 | 0 | 18-Sep-14 A | | |
| LL2-2068 | LL2 - Generator Room - Electrical Finishes | 3 | 0 | 19-Sep-14 A | 30-Sep-14 A | |
| L07-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L09-7026 | Inspections for GWB Cover | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L04-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L05-7122 | HVAC Rough-In | 1 | 0 | 22-Sep-14 A | 22-Sep-14 A | |
| L03-8140 | Countertops On Site | 0 | 0 | 22-Sep-14 A | | |
| L03-8129a | Shower Doors On Site | 0 | 0 | 22-Sep-14 A | | |
| LL1-Z3-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L1BOH2-6028 | Framing at Elevator Lobby | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2-2048a | LL2 - Move in Laundry Room Ironer | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| LL2E-8122 | LL2 - Hang GWB at Fire Pump Room | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-FCC20 | FCC - Rough-In and Install Panels | 25 | 0 | 22-Sep-14 A | 21-Nov-14 A | |
| I-3014 | Core drill for MEP relocations | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L05-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L07-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 05-Dec-14 A | |
| L09-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 05-Dec-14 A | |
| L14-7028 | GWB Hang/Tape/Finish | 5 | 0 | 23-Sep-14 A | 08-Dec-14 A | |
| L04-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |
| L05-7120 | Electrical Rough-In | 2 | 0 | 23-Sep-14 A | 24-Sep-14 A | |

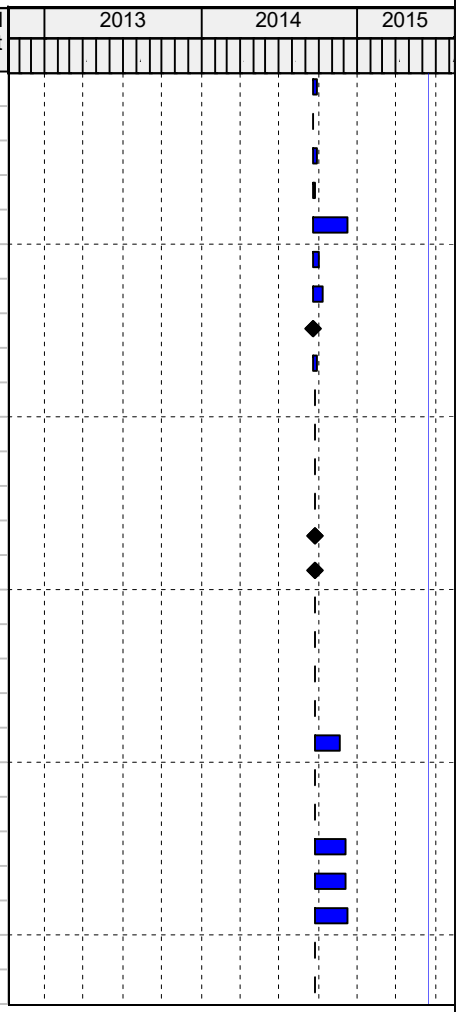


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L07-7122 | HVAC Rough-In | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| ASI53ca | ASI No. 53 - Pool Chemical Storage System (City Apr | 0 | 0 | 23-Sep-14 A | | |
| L04-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L06-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-8201 | Install ACT Grid @ Corridors | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L04-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L05-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L06-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L07-7120 | Electrical Rough-In | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L08-7122 | HVAC Rough-In | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| LL1-Z3-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| LL2-2058 | LL2 - Tape/Finish Laundry Room | 3 | 0 | 24-Sep-14 A | 26-Sep-14 A | |
| I-5034 | RFI 717 - Porte Cochere Paving Details | 1 | 0 | 24-Sep-14 A | 29-Oct-14 A | |
| L08-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L17-8395 | Framing at Elevator Lobby | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L05-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| L06-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L07-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 25-Sep-14 A | 25-Sep-14 A | |
| L08-7120 | Electrical Rough-In | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| LL2E-8124 | LL2 - Temp-In Louver Opening at Fire Pump Room | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L1-5104c | L1 - Install Storefront at Main Entry Facade | 5 | 0 | 25-Sep-14 A | 10-Oct-14 A | |
| I-5030 | RFI 715 - Additional Site Paving Per City | 1 | 0 | 25-Sep-14 A | 14-Oct-14 A | |
| L16-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |

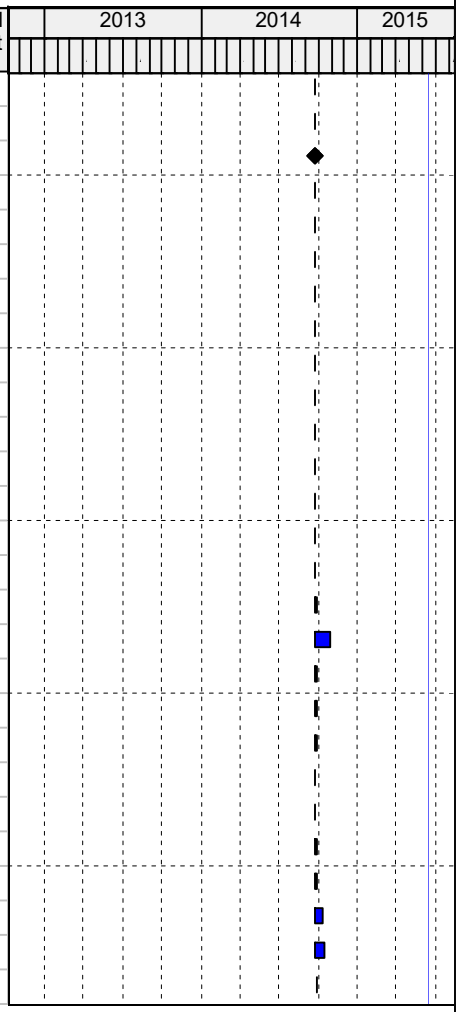



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L10-7122 | HVAC Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L16-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L17-7124 | Fire Sprinkler Rough-In | 1 | 0 | 26-Sep-14 A | 26-Sep-14 A | |
| L09-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L17-8403 | Fire Sprinkler Rough-In at Elevator Lobby | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L09-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-8201 | Install ACT Grid @ Corridors | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L09-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L10-7120 | Electrical Rough-In | 2 | 0 | 29-Sep-14 A | 30-Sep-14 A | |
| L11-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L12-7122 | HVAC Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L14-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L15-7124 | Fire Sprinkler Rough-In | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| L17-7118 | Install HM Door Frame | 1 | 0 | 29-Sep-14 A | 29-Sep-14 A | |
| LL3-6030 | LL3 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL4-6030 | LL4 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| LL2-6034 | LL2 - Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L1BOH2-6030 | Electrical RI at Elevator Lobby | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L02-6030 | L2 - Framing at Elevator Lobby & North Half | 4 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| MPT-1022 | Tower - Caulking, west | 8 | 0 | 29-Sep-14 A | 03-Nov-14 A | |
| PH-6015 | PH - Set Boilers and Pumps | 12 | 0 | 29-Sep-14 A | 15-Oct-14 A | |
| L11-8204 | Bathrooms - Vinyl Wall Coverings | 2 | 0 | 29-Sep-14 A | 02-Oct-14 A | |
| L10-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L17-6034 | Insulation & Fire Caulk at Heat Pumps | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |

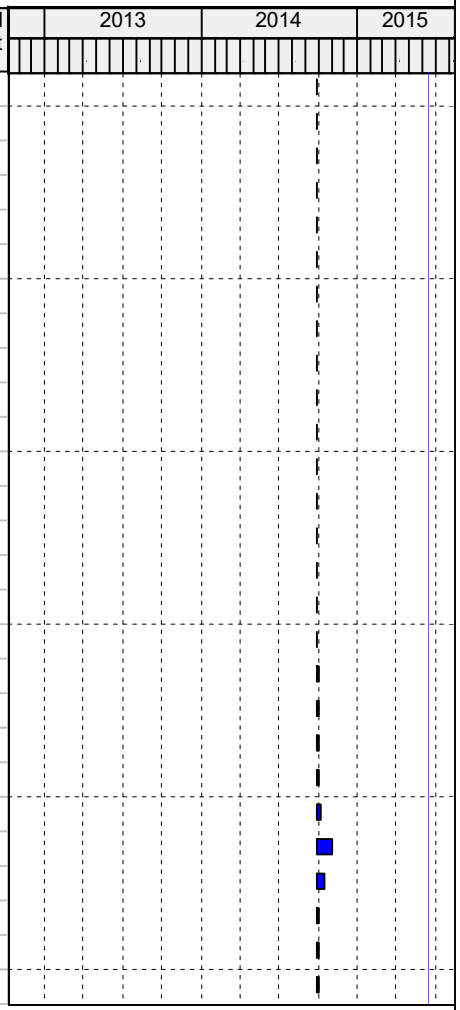



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L12-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L07-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 30-Sep-14 A | 08-Oct-14 A | |
| L11-8201 | Install ACT Grid @ Corridors | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L09-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L09-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7124 | Fire Sprinkler Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L10-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L11-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L12-7120 | Electrical Rough-In | 2 | 0 | 30-Sep-14 A | 01-Oct-14 A | |
| L14-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| L15-7122 | HVAC Rough-In | 1 | 0 | 30-Sep-14 A | 30-Sep-14 A | |
| LL2-2072 | Generator - Complete generator and annunciator cor | 5 | 0 | 30-Sep-14 A | 21-Oct-14 A | |
| L17-6040 | Test Heat Pumps - L16 and L17 | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L17-6036 | Framing Around Heat Pump & Soffit | 3 | 0 | 01-Oct-14 A | 06-Oct-14 A | |
| L14-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L03-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L03-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L04-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L05-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |

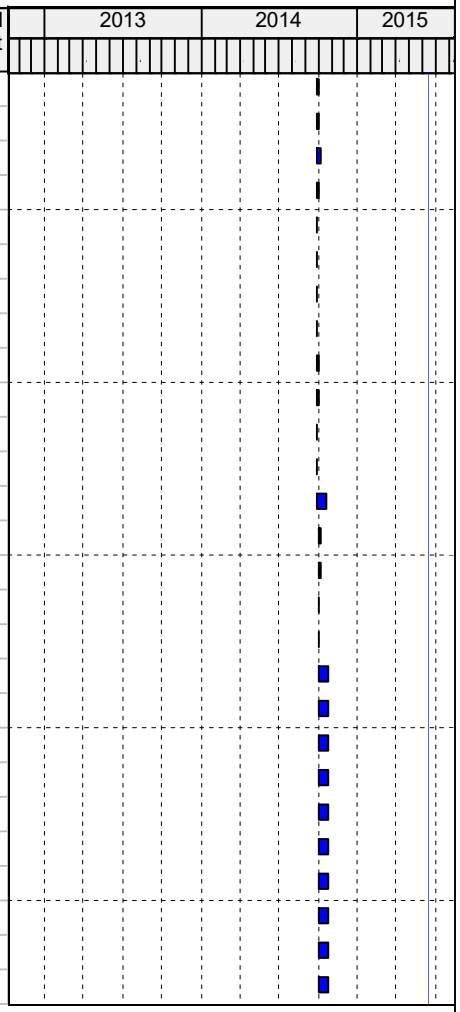



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L06-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L07-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L08-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L09-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L10-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L12-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L14-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L15-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 01-Oct-14 A | 24-Oct-14 A | |
| L11-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |

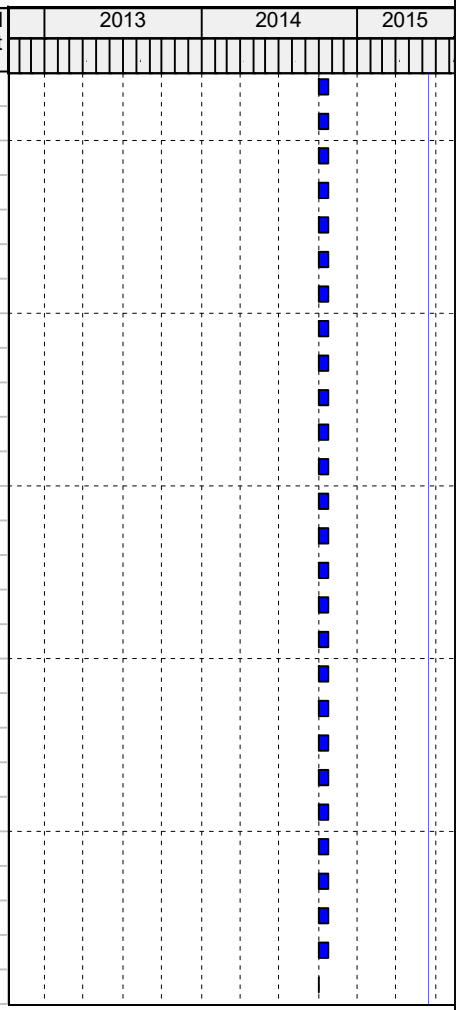



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L12-7124 | Fire Sprinkler Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L12-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L14-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L15-7120 | Electrical Rough-In | 2 | 0 | 01-Oct-14 A | 02-Oct-14 A | |
| L16-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L17-7122 | HVAC Rough-In | 1 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L09-8136 | Install Counter Subtops | 3 | 0 | 01-Oct-14 A | 03-Oct-14 A | |
| L02-6032 | L2 - Electrical RI at Elevator Lobby & North Half | 5 | 0 | 01-Oct-14 A | 08-Oct-14 A | |
| SW-2306 | Prep, grind and overlay at 11th Ave, 3rd Place & 2nd | 5 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 01-Oct-14 A | 01-Oct-14 A | |
| L05-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 01-Oct-14 A | 16-Dec-14 A | |
| L16-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-8402 | Electrical Rough-In at Elevator Lobby | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L14-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L15-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L17-7120 | Electrical Rough-In | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1BOH2-8130 | Inspections For Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L02-6024a | L2 - Inspections - South Half | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L06-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 02-Oct-14 A | 02-Oct-14 A | |
| L16-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| L17-7126 | Fire Alarm / Elec Specialties Rough-In | 1 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| LL2-2074 | Generator - Install fuel fill | 2 | 0 | 03-Oct-14 A | 06-Oct-14 A | |
| L07-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| MPT-1020 | Tower - Install E/W Wing, East End (Elev 41,44) | 5 | 0 | 06-Oct-14 A | 18-Oct-14 A | |
| LL1-8102a | GWB Hang/Tape (Ceilings) | 10 | 0 | 06-Oct-14 A | 18-Nov-14 A | |

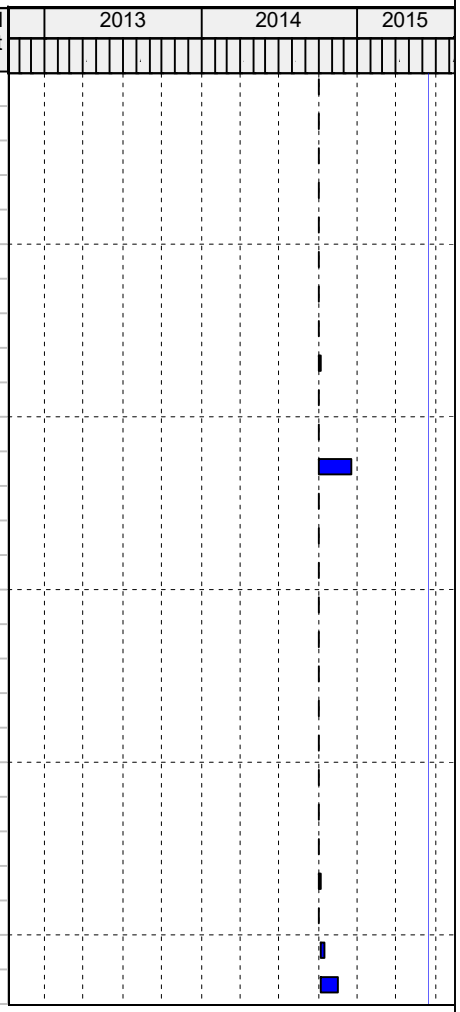



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1BOH2C-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6014 | Complete Plumbing RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6016 | Complete Electrical RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6018 | Complete HVAC RI @ Ceilings & Inspection | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L1BOH2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| L03-8200a | New murals on site (date estimated) | 0 | 0 | 06-Oct-14 A | | |
| SW-2100 | Zone 1 - Survey curb & site lighting | 2 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 06-Oct-14 A | 06-Oct-14 A | |
| L1BOH2-8100 | Insulation | 4 | 0 | 07-Oct-14 A | 13-Oct-14 A | |
| L17-6038 | Electrical at Heat Pump & Soffit | 1 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L12-8201 | Install ACT Grid @ Corridors | 2 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| L10-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 07-Oct-14 A | 20-Oct-14 A | |
| L03-8216x | Vinyl Wall Coverings - Install Murals | 2 | 0 | 07-Oct-14 A | 29-Dec-14 A | |
| L1B-8102b | GWB Hang (Walls) & Inspection - Exterior Wall at Cor | 3 | 0 | 07-Oct-14 A | 09-Oct-14 A | |
| RF-4048 | Tower Roof - Install davit arms | 3 | 0 | 07-Oct-14 A | 08-Oct-14 A | |
| LL2-2076 | Generator - Install fuel fill mechanical piping | 4 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L12-8204 | Bathrooms - Vinyl Wall Covering | 2 | 0 | 07-Oct-14 A | 10-Oct-14 A | |
| L09-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 07-Oct-14 A | 07-Oct-14 A | |
| L03-8633 | Pool - Install waterproofing & test | 3 | 0 | 08-Oct-14 A | 17-Oct-14 A | |
| L03-8130 | Install Door Hardware | 3 | 0 | 08-Oct-14 A | 28-Oct-14 A | |
| L10-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L02-8102a | L2 - GWB Hang / Tape / Finish - South Half | 7 | 0 | 09-Oct-14 A | 27-Oct-14 A | |
| SW-2102 | Zone 1 - Vacate SE corner | 2 | 0 | 09-Oct-14 A | 11-Oct-14 A | |
| SW-2106 | Zone 1 - Sawcut and remove asphalt | 4 | 0 | 09-Oct-14 A | 14-Oct-14 A | |
| L11-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 09-Oct-14 A | |
| SW-2200 | Zone 2 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |
| SW-2300 | Zone 3 - Sawcut asphalt | 3 | 0 | 10-Oct-14 A | 14-Oct-14 A | |

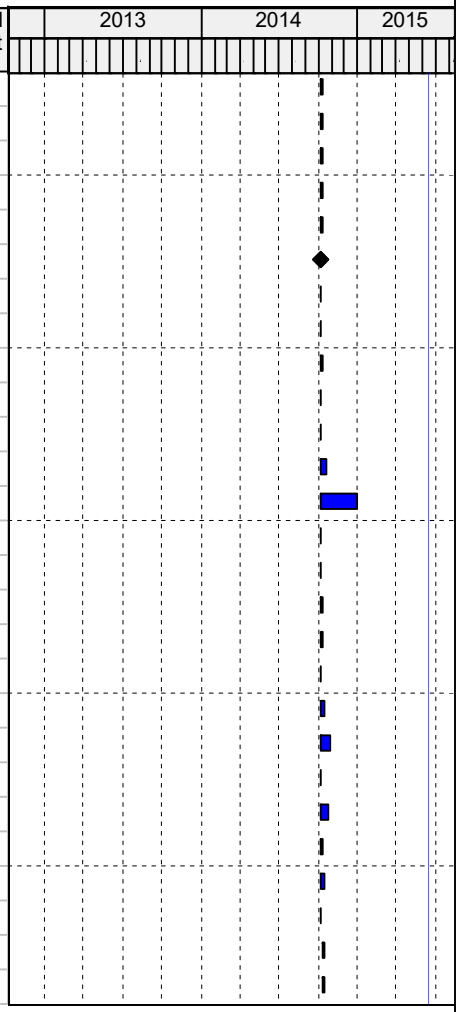



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2108 | Zone 1 - Install east footing drain | 4 | 0 | 10-Oct-14 A | 20-Oct-14 A | |
| L04-8130 | Install Door Hardware | 3 | 0 | 10-Oct-14 A | 29-Oct-14 A | |
| ML-5962 | Man/Material Lifts - Remove Roof Lift Stop | 0 | 0 | | 11-Oct-14 A | |
| I-1102 | Additional work at new L17 guest rooms | 5 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| LL2-2046 | LL2 - Generator Room - Misc. Finishes | 3 | 0 | 13-Oct-14 A | 21-Nov-14 A | |
| RF-4008 | Tower Roof - Install corrugated metal panels | 5 | 0 | 13-Oct-14 A | 03-Nov-14 A | |
| MPT-1018b | Tower - Roof cornice frame & sheath | 6 | 0 | 13-Oct-14 A | 24-Oct-14 A | |
| L02-8100a | L2 - Insulation - South Half | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| SW-2112 | Zone 1 - Grade for curb and gutter | 3 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| SW-2202 | Zone 2 - Install site lighting | 5 | 0 | 13-Oct-14 A | 24-Nov-14 A | |
| SW-2204 | Zone 2 - Repave utility trenches | 4 | 0 | 13-Oct-14 A | 22-Oct-14 A | |
| L12-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 13-Oct-14 A | |
| I-5038 | RFI 735 - Landscape Irrigation Conflict | 1 | 0 | 13-Oct-14 A | 03-Nov-14 A | |
| SW-2302 | Zone 3 - Grade for curb and gutter | 2 | 0 | 14-Oct-14 A | 01-Dec-14 A | |
| L14-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 14-Oct-14 A | 16-Oct-14 A | |
| L05-8130 | Install Door Hardware | 3 | 0 | 14-Oct-14 A | 03-Nov-14 A | |
| L14-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 14-Oct-14 A | |
| I-5032 | RFI 715.1 - Additional Site Paving Per City | 1 | 0 | 14-Oct-14 A | 29-Oct-14 A | |
| L16-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L16-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7036 | Install Electrical Transformers, Bus Duct, Panelboards | 3 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7038 | Electrical Terminations & Trim-Out | 2 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L17-7040 | Fire Alarm / Elec Specialties Terminations & Trim-Out | 5 | 0 | 15-Oct-14 A | 27-Oct-14 A | |
| L15-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 15-Oct-14 A | 17-Oct-14 A | |
| L15-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 15-Oct-14 A | |
| SW-2206 | Zone 2 - Grade for curb and gutter | 2 | 0 | 16-Oct-14 A | 20-Oct-14 A | |

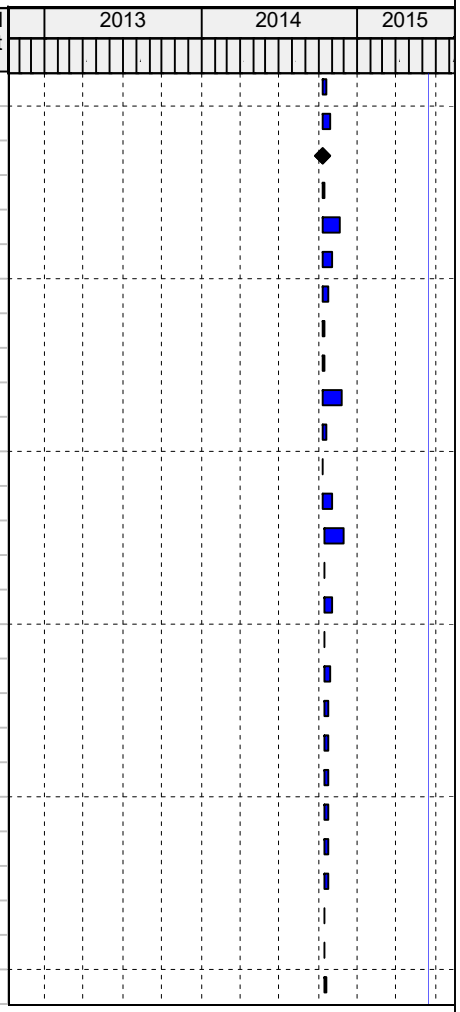



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-5598 | Resolve FCC hard lid ceiling issue (RFI 734) | 1 | 0 | 16-Oct-14 A | 16-Nov-14 A | |
| ASI57 | ASI No. 57 - MDP Electrical Revisions Rev. 22 | 0 | 0 | 17-Oct-14 A | | |
| MPP-1000 | Podium - Install W/S/N Elevations (Elev 1-5, 6,9-19,2 | 10 | 0 | 20-Oct-14 A | 10-Dec-14 A | |
| L06-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 20-Oct-14 A | 23-Oct-14 A | |
| LL2-8106a | LL2, Garage - Pinned Insulation (except at ramp) | 4 | 0 | 20-Oct-14 A | 04-Dec-14 A | |
| L1B-8102d | GWB Hang (Walls) & Inspection - Main Ballroom East | 1 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| SW-2114 | Zone 1 - FRP curb and gutter | 2 | 0 | 20-Oct-14 A | 14-Nov-14 A | |
| RF-4044 | Ballroom Roof - Install metal coping | 3 | 0 | 20-Oct-14 A | 13-Nov-14 A | |
| L08-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 21-Oct-14 A | 23-Oct-14 A | |
| MPT-1018 | Tower - Install Roof Penthouse (Elev 36b,37,38.39) | 5 | 0 | 21-Oct-14 A | 05-Dec-14 A | |
| L11-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2208 | Zone 2 - FRP curb and gutter | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| SW-2304 | Zone 3 - FRP curb and gutter | 3 | 0 | 21-Oct-14 A | 02-Dec-14 A | |
| L15-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L06-8130 | Install Door Hardware | 3 | 0 | 21-Oct-14 A | 03-Nov-14 A | |
| I-5100 | Resolve changes (ASI's and RFI's) | 1 | 0 | 21-Oct-14 A | 07-Jan-15 A | |
| L03-8634 | Pool - Install reinforcing steel & inspect | 5 | 0 | 22-Oct-14 A | 30-Oct-14 A | |
| MPT-1016 | Tower - Install N/S Wing, S. End W. of Manlift (Elev 2 | 5 | 0 | 22-Oct-14 A | 05-Dec-14 A | |
| SW-2116 | Zone 1 - Fine grade for sidewalk | 3 | 0 | 22-Oct-14 A | 09-Mar-15 A | |
| LL4-8106 | LL4 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| LL3-8106 | LL3 - Insulation and air barrier | 3 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L14-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 22-Oct-14 A | 24-Oct-14 A | |
| L08-8130 | Install Door Hardware | 3 | 0 | 22-Oct-14 A | 04-Nov-14 A | |
| L07-8130 | Install Door Hardware | 3 | 0 | 22-Oct-14 A | 03-Nov-14 A | |
| ASI54 | ASI No. 54 - Architectural Revisions for Lobby and Cl | 0 | 0 | 22-Oct-14 A | | |
| ASI55 | ASI No. 55 - Kay Lang Interior Concierge and Lobby | 0 | 0 | 22-Oct-14 A | | |
| L03-8606 | L3 Pool - HVAC R/I | 3 | 0 | 23-Oct-14 A | 27-Oct-14 A | |

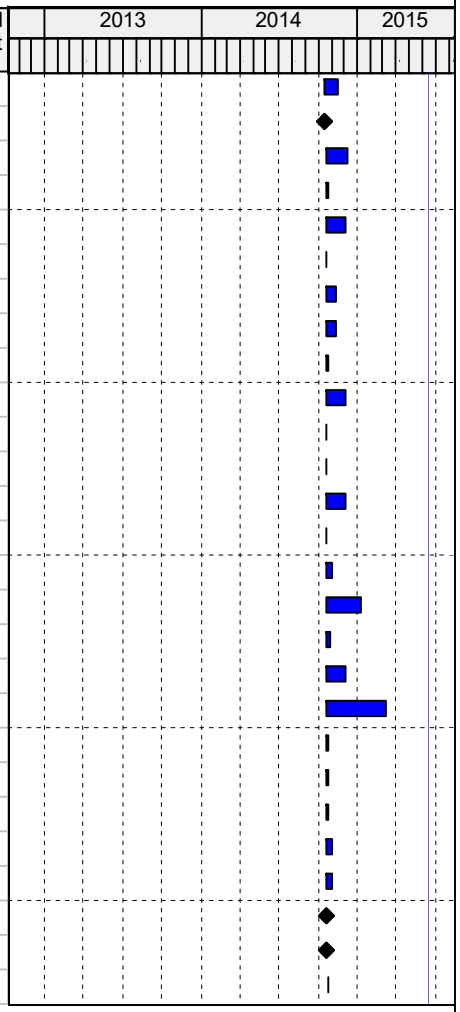



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 23-Oct-14 A | 03-Nov-14 A | |
| L12-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| LL2-2078 | Generator - Install fuel fill control wiring | 2 | 0 | 23-Oct-14 A | 24-Oct-14 A | |
| I-2950 | Kitchen Hood Type 1 impact (COB correction notice, I | 1 | 0 | 23-Oct-14 A | 21-Dec-14 A | |
| RF-4050 | Roof at Manlift - Erect steel | 1 | 0 | 24-Oct-14 A | 24-Oct-14 A | |
| CO-7204 | Cx - Gas Service established | 0 | 0 | | 24-Oct-14 A | |
| I-5900 | Owner select color for Porte Cochere drive concrete | 20 | 0 | 24-Oct-14 A | 11-Mar-15 A | |
| L1BOH2-8102 | GWB Hang (Walls) | 4 | 0 | 27-Oct-14 A | 07-Nov-14 A | |
| L04-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 27-Oct-14 A | 12-Nov-14 A | |
| RF-4052 | Roof at Manlift - Framing/sheathing/air barrier (inspec | 4 | 0 | 27-Oct-14 A | 30-Oct-14 A | |
| LL2-2080 | Generator - Complete generator accessories (battery) | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| LL2-2082 | Generator - Cx fuel fill | 1 | 0 | 27-Oct-14 A | 27-Oct-14 A | |
| L09-8130 | Install Door Hardware | 3 | 0 | 28-Oct-14 A | 04-Nov-14 A | |
| CO-7158 | Generator - Interim electrical inspection | 1 | 0 | 29-Oct-14 A | 29-Oct-14 A | |
| LL2-2070 | LL2 - Generator Room - Generator Ready for Startup | 0 | 0 | | 30-Oct-14 A | |
| LL2-2084 | Generator - Initial fuel fill | 1 | 0 | 30-Oct-14 A | 30-Oct-14 A | |
| CO-7200 | Cx - Penthouse Mechanical Installation Complete | 0 | 0 | | 30-Oct-14 A | |
| EL-6028 | Elev 6 - RFI-761: Response, pricing, complete work (r | 20 | 0 | 30-Oct-14 A | 27-Jan-15 A | |
| L03-8636 | Pool - Shotcrete | 1 | 0 | 31-Oct-14 A | 31-Oct-14 A | |
| RF-4054 | Roof at Manlift - Final mechanical installations | 4 | 0 | 31-Oct-14 A | 05-Nov-14 A | |
| RF-4056 | Roof at Manlift - Final electrical connections | 2 | 0 | 31-Oct-14 A | 05-Nov-14 A | |
| CO-7130 | Fire Alarm - Point-To-Point Wiring | 18 | 0 | 01-Nov-14 A | 06-Feb-15 A | |
| L03-8404 | GWB Hang/Tape Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 14-Nov-14 A | |
| L04-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 14-Nov-14 A | |
| L05-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 17-Nov-14 A | |
| L06-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 03-Nov-14 A | 17-Nov-14 A | |
| L03-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |

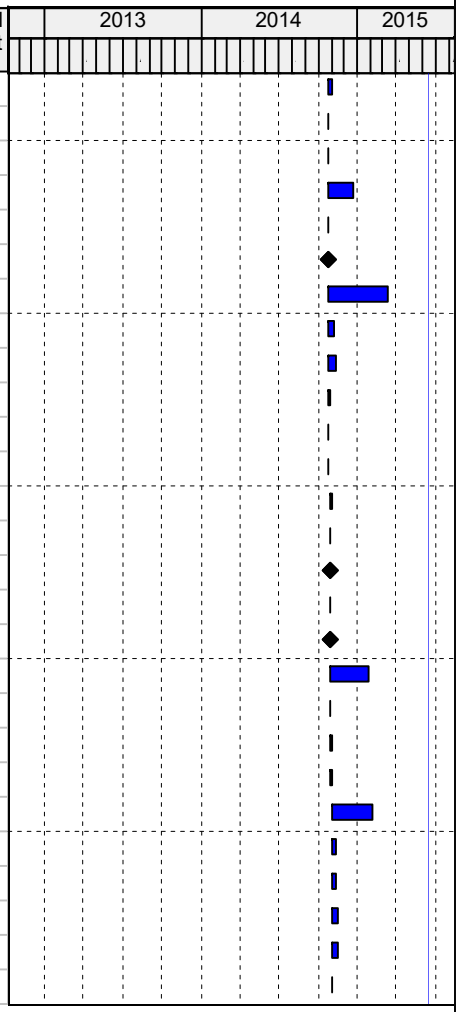



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L05-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L06-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L07-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L08-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L09-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L10-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L11-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L12-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L14-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L15-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L16-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L17-8405 | Cover Inspection | 1 | 0 | 03-Nov-14 A | 03-Nov-14 A | |
| L14-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 03-Nov-14 A | 06-Nov-14 A | |
| MPT-1024 | (A) Caulking - Elevation 41 (east elevation above poo | 7 | 0 | 03-Nov-14 A | 16-Dec-14 A | |
| CO-7206 | Cx - Purge/Prove Gas-Fed Equipment and Feeder Li | 7 | 0 | 03-Nov-14 A | 09-Nov-14 A | |
| I-5200 | Resolve MEP conflicts with ceiling grid (RFIs 783 & 8 | 8 | 0 | 03-Nov-14 A | 18-Mar-15 A | |
| I-5040 | RFI 776 - North Sidewalk-Entrance Conflicts | 1 | 0 | 03-Nov-14 A | 18-Dec-14 A | |
| L07-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 17-Nov-14 A | |
| L08-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L09-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L10-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 04-Nov-14 A | 18-Nov-14 A | |
| L12-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L11-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 04-Nov-14 A | 15-Dec-14 A | |
| L11-8130 | Install Door Hardware | 3 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L10-8130 | Install Door Hardware | 3 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L11-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 18-Nov-14 A | |

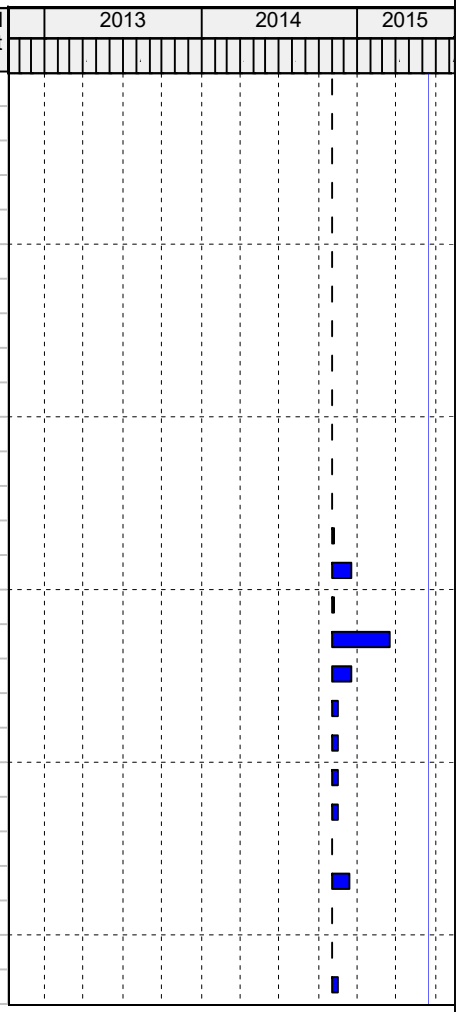



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 19-Nov-14 A | |
| L14-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 05-Nov-14 A | 19-Nov-14 A | |
| MPP-1010 | Podium - Install East Elevation (Elev 5 & 7) | 7 | 0 | 05-Nov-14 A | 10-Dec-14 A | |
| CO-7162 | Generator - Load bank testing | 1 | 0 | 05-Nov-14 A | 05-Nov-14 A | |
| CO-7202 | Cx - Electrical Internal Bus & LL2-L17 Bus Duct Energ | 0 | 0 | | 05-Nov-14 A | |
| CO-7202a | Cx - Energize normal power distribution | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| I-5036 | RFI 717.1 - Porte Cochere Paving Details | 1 | 0 | 05-Nov-14 A | 26-Nov-14 A | |
| L15-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 19-Nov-14 A | |
| L16-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 20-Nov-14 A | |
| L17-8404 | GWB Hang/Tape/Finish at Elevator Lobby | 5 | 0 | 06-Nov-14 A | 20-Nov-14 A | |
| RF-4058 | Roof at Manlift - Install roofing | 2 | 0 | 06-Nov-14 A | 07-Nov-14 A | |
| CO-7164 | Generator - Final electrical inspection | 1 | 0 | 06-Nov-14 A | 06-Nov-14 A | |
| ASI59 | ASI No. 59 - Electrical One-Line Revisions | 0 | 0 | 06-Nov-14 A | | |
| I-5042 | RFI 796 - City Requested Added Scope | 1 | 0 | 06-Nov-14 A | 22-Dec-14 A | |
| I-5046 | RFI 803 - Site Light Bases Layout with Existing Sidew | 1 | 0 | 06-Nov-14 A | 14-Jan-15 A | |
| L15-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 07-Nov-14 A | 12-Nov-14 A | |
| L03-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L03-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L04-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L04-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L05-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L05-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L06-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L06-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L07-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L07-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 03-Dec-14 A | |
| L08-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |

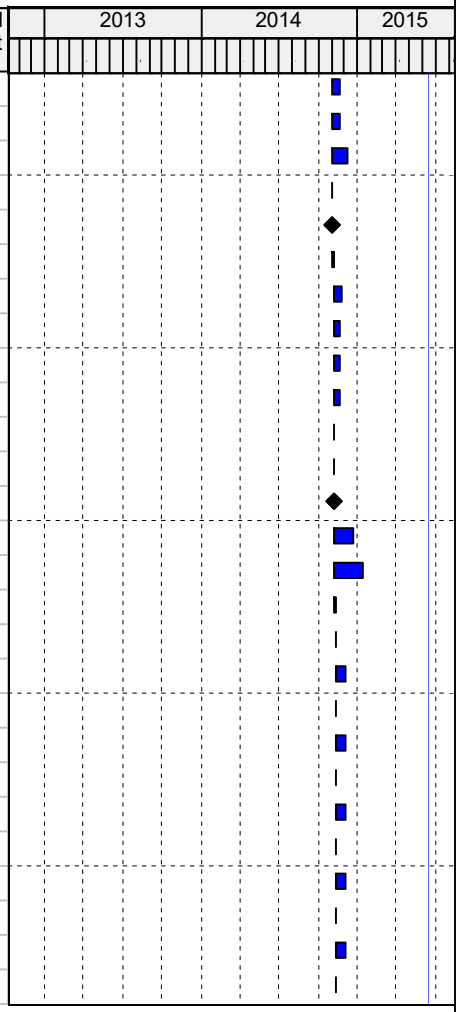



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L09-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L09-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L10-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L10-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L11-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L11-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 05-Dec-14 A | |
| L12-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L12-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L14-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L14-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L15-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L15-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L16-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L16-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L17-7128 | Inspections for GWB Cover | 1 | 0 | 10-Nov-14 A | 10-Nov-14 A | |
| L17-7130 | GWB Hang/Tape/Finish | 5 | 0 | 10-Nov-14 A | 12-Dec-14 A | |
| L05-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| L06-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 10-Nov-14 A | 11-Nov-14 A | |
| MPT-1032 | Tower - Install sign backing NW (Elev 51,52) | 4 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L12-8130 | Install Door Hardware | 3 | 0 | 10-Nov-14 A | 12-Nov-14 A | |
| EL-1230 | Elev 1&2 - Complete hoistway ventilation | 13 | 0 | 10-Nov-14 A | 15-Dec-14 A | |
| EL-1232 | Elev 1&2 - Wire & startup AC split units | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-1234 | Elev 1&2 - Install EMR doors, hardware & labeling | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-3428 | Elev 3&4 - Complete hoistway ventilation | 13 | 0 | 10-Nov-14 A | 15-Dec-14 A | |
| EL-3430 | Elev 3&4 - Wire & startup AC split units | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| EL-3432 | Elev 3&4 - Install EMR doors, hardware & labeling | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |

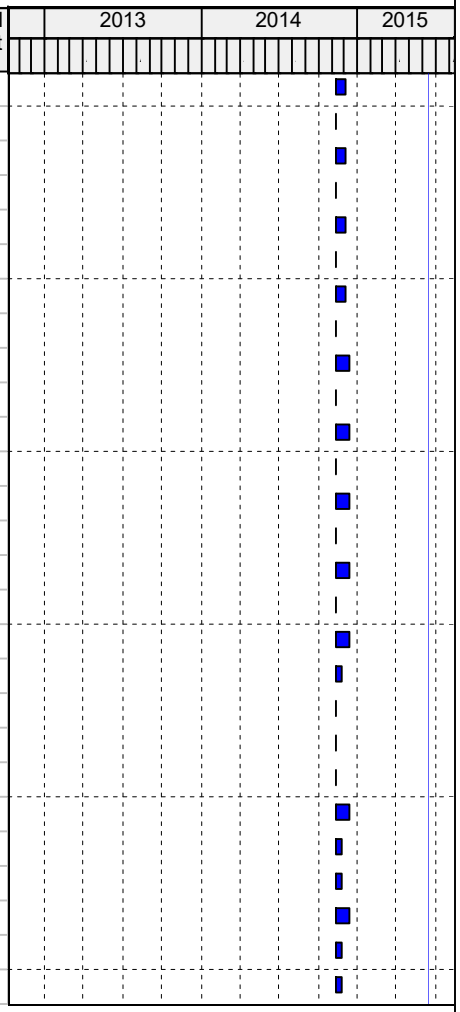



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-6030 | Elev 6 - Complete fire-rated assemblies at hoistway, l | 13 | 0 | 10-Nov-14 A | 26-Nov-14 A | |
| L07-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 11-Nov-14 A | 12-Nov-14 A | |
| L16-8106 | Paint - Accent Walls | 2 | 0 | 11-Nov-14 A | 12-Nov-14 A | |
| L14-8130 | Install Door Hardware | 3 | 0 | 11-Nov-14 A | 13-Nov-14 A | |
| I-5044 | RFI 802 - Landscape Planter & Arch Detail Coordinati | 1 | 0 | 11-Nov-14 A | 18-Nov-14 A | |
| L03-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 12-Nov-14 A | 18-Nov-14 A | |
| SW-2104 | Zone 1 - Install lighting conduit at SE corner | 2 | 0 | 12-Nov-14 A | 14-Nov-14 A | |
| L16-8111 | Paint - Door Jambs | 2 | 0 | 12-Nov-14 A | 13-Nov-14 A | |
| EL-6010i | Elev 6 - Pit Slab Correction (form/pour/strip/clean) | 10 | 0 | 12-Nov-14 A | 26-Nov-14 A | |
| SW-2024 | Zone 4 - FRP Porte Cochere planter & bench | 6 | 0 | 12-Nov-14 A | 04-Dec-14 A | |
| L08-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| SW-2109 | Zone 1 - Install irrigation sleeves | 2 | 0 | 13-Nov-14 A | 14-Nov-14 A | |
| MPT-1026 | (C) Caulking - Elevation 47 (north elevation, east half | 10 | 0 | 13-Nov-14 A | 19-Dec-14 A | |
| L16-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| L15-8130 | Install Door Hardware | 3 | 0 | 13-Nov-14 A | 18-Nov-14 A | |
| ASI56 | ASI No. 56 - Interior Design Millwork and Finish Chan | 0 | 0 | 13-Nov-14 A | | |
| L04-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 14-Nov-14 A | 19-Nov-14 A | |
| SW-2203 | Zone 2 - Install irrigation sleeves | 2 | 0 | 14-Nov-14 A | 08-Jan-15 A | |
| L1B-8120 | Install operable partitions | 3 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| LL1-Z3-8340 | Install walk-in cooler/freezer (BY OTHERS) | 5 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| SW-2316 | Zone 3 - Demolish manlift shack and base | 5 | 0 | 17-Nov-14 A | 20-Nov-14 A | |
| I-1610 | Enclosure at manlift - Install exterior wall panels & ins | 5 | 0 | 17-Nov-14 A | 21-Nov-14 A | |
| L04-8140 | Install window sills | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| L03-8140x | Install window sills | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| L16-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 17-Nov-14 A | 17-Nov-14 A | |
| SW-2014 | Porte Cochere - Electrical rough-in | 5 | 0 | 17-Nov-14 A | 08-Dec-14 A | |
| I-5600 | Lower heat pump and install access panels (RFI 734) | 13 | 0 | 17-Nov-14 A | 09-Jan-15 A | |

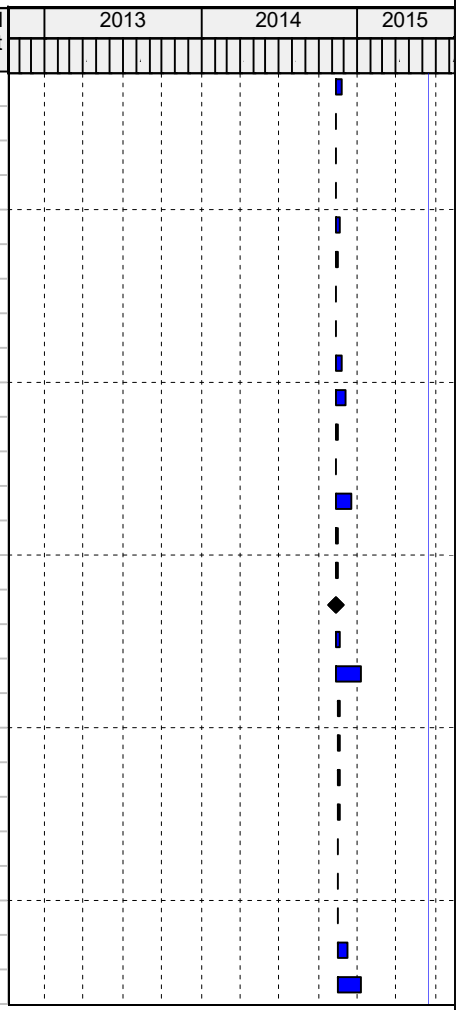



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-FCC26 | Program FACP & Stand-Up System | 20 | 0 | 17-Nov-14 A | 22-Jan-15 A | |
| L06-8140 | Install window sills | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L05-8140 | Install window sills | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| I-5048 | RFI 805 - City Approved Public ROW Irrigation Lines I | 1 | 0 | 18-Nov-14 A | 05-Dec-14 A | |
| L05-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 19-Nov-14 A | 22-Dec-14 A | |
| L16-8130 | Install Door Hardware | 3 | 0 | 19-Nov-14 A | 02-Dec-14 A | |
| L08-8140 | Install window sills | 2 | 0 | 19-Nov-14 A | 19-Nov-14 A | |
| L07-8140 | Install window sills | 2 | 0 | 19-Nov-14 A | 19-Nov-14 A | |
| I-1616 | Enclosure at manlift - Patch/repair concrete shear wal | 3 | 0 | 19-Nov-14 A | 21-Nov-14 A | |
| ASI58 | ASI No. 58 - Level 1 Valet Phone and POS Locations | 0 | 0 | 19-Nov-14 A | | |
| ASI59ca | ASI No. 59 - Electrical One-Line Revisions (City Appro | 0 | 0 | 19-Nov-14 A | | |
| L10-8140 | Install window sills | 2 | 0 | 20-Nov-14 A | 20-Nov-14 A | |
| L09-8140 | Install window sills | 2 | 0 | 20-Nov-14 A | 20-Nov-14 A | |
| I-1622 | Manlift finishes - Install windows & caulk | 4 | 0 | 20-Nov-14 A | 03-Dec-14 A | |
| LL2-2060 | LL2 - Paint Laundry Room | 3 | 0 | 21-Nov-14 A | 24-Nov-14 A | |
| L03-8616 | L3 Pool - GWB above ceiling | 2 | 0 | 21-Nov-14 A | 22-Nov-14 A | |
| LL1-Z3-8342 | Final connections at walk-in cooler/freezer | 2 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L1K-8340 | Install walk-in cooler/freezer (BY OTHERS) | 2 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L10-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| L16-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| SW-2110 | Zone 1 - Adjust utilities structures | 5 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| SW-2214 | Zone 2 - Adjust utilities structures | 2 | 0 | 24-Nov-14 A | 25-Nov-14 A | |
| MPT-1030 | Tower - Install sign backing NE (Elev 44) | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| SW-2012 | Porte Cochere - Install cornice[DELETED SEE REV M | 8 | 0 | 24-Nov-14 A | 05-Dec-14 A | |
| L03-8650 | L3 Pool - Build scaffold at pool pit | 2 | 0 | 24-Nov-14 A | 25-Nov-14 A | |
| EL-6032 | Elev 6 - Install pit ladder | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| EL-6034 | Elev 6 - Install pit jack & hoistway pistons; connect hy | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |

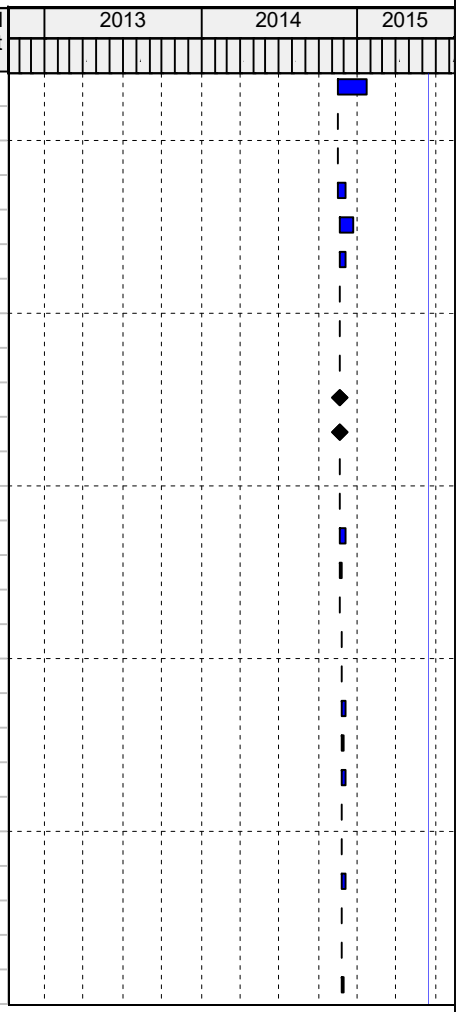


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 25-Nov-14 A | 22-Dec-14 A | |
| L02-8104a | L2 - Int Painting - South Half | 2 | 0 | 25-Nov-14 A | 26-Nov-14 A | |
| SW-2016 | Porte Cochere - Complete framing | 3 | 0 | 25-Nov-14 A | 01-Dec-14 A | |
| LL2-2096 | LL2 - Install FRP at Laundry Room | 8 | 0 | 25-Nov-14 A | 05-Dec-14 A | |
| I-1602 | Enclosure at manlift - Install shear wall clips and inspe | 4 | 0 | 26-Nov-14 A | 05-Dec-14 A | |
| L07-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| SW-2318 | Zone 3 - Install catch basin | 1 | 0 | 26-Nov-14 A | 26-Nov-14 A | |
| L03-8652 | L3 Pool - Frame ceiling | 4 | 0 | 26-Nov-14 A | 04-Dec-14 A | |
| I-5052 | RFI 819 - Flagpole Locations | 1 | 0 | 26-Nov-14 A | 30-Dec-14 A | |
| I-5050 | RFI 818 - 111th East Elevation Hardscape Vertical Dif | 1 | 0 | 26-Nov-14 A | 29-Dec-14 A | |
| L03-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L04-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L05-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L06-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L07-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L09-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L10-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L11-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L12-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L14-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L15-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L16-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L17-8412 | Final Coat Finish Paint at Elevator Lobby [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 01-Dec-14 A | 04-Dec-14 A | |
| L02-6016a | L2 - Electrical Room Buildout | 5 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| L03-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |

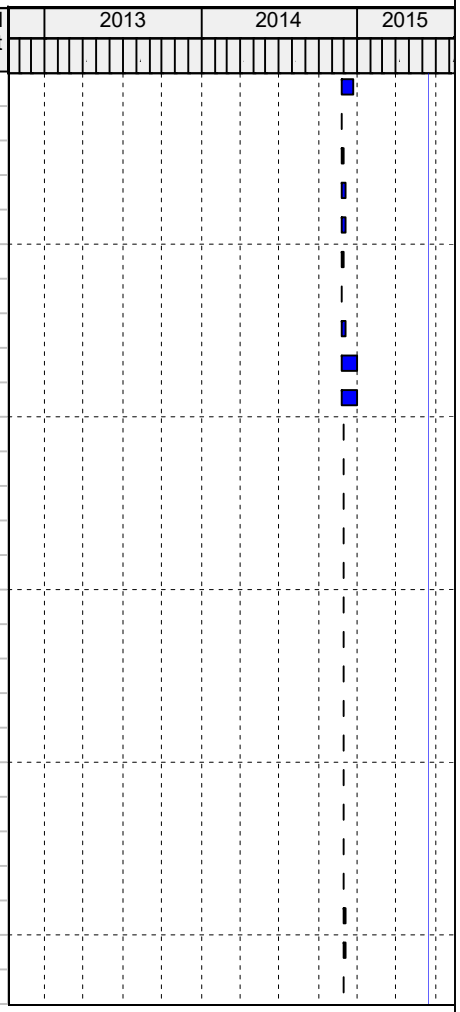



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L05-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L06-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L07-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L08-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L09-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L10-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L11-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L12-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L14-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L15-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L16-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| L17-7146 | Final Coat Finish Paint [DELETED] | 2 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| SW-2210 | Zone 2 - Fine grade for sidewalk | 5 | 0 | 01-Dec-14 A | 08-Jan-15 A | |
| RF-4040 | L2.5 Horseshoe - Install sheet metal capping[DELETI | 3 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| MPT-1042 | Enclosure at manlift - air barrier & inspect | 5 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| CO-7208 | Cx - Start-Up Pumps | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| CO-7210 | Cx - Start-Up VFD's | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| L17-8106 | Paint - Accent Walls | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| LL4-8116 | LL4 - Install ACT grid [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL3-8116 | LL3 - Install ACT grid [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| I-1630 | Manlift finishes - Framing, corridor ceilings & inspect | 4 | 0 | 01-Dec-14 A | 09-Dec-14 A | |
| EL-6036 | Elev 6 - Install shunt trip breaker | 5 | 0 | 01-Dec-14 A | 05-Dec-14 A | |
| L17-8111 | Paint - Door Jambs | 2 | 0 | 02-Dec-14 A | 03-Dec-14 A | |
| SW-2018 | Porte Cochere - GWB hang/tape | 3 | 0 | 02-Dec-14 A | 09-Dec-14 A | |
| L03-8654 | L3 Pool - HVAC drops at ceiling & inspect | 3 | 0 | 02-Dec-14 A | 05-Dec-14 A | |
| L11-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 03-Dec-14 A | 08-Dec-14 A | |

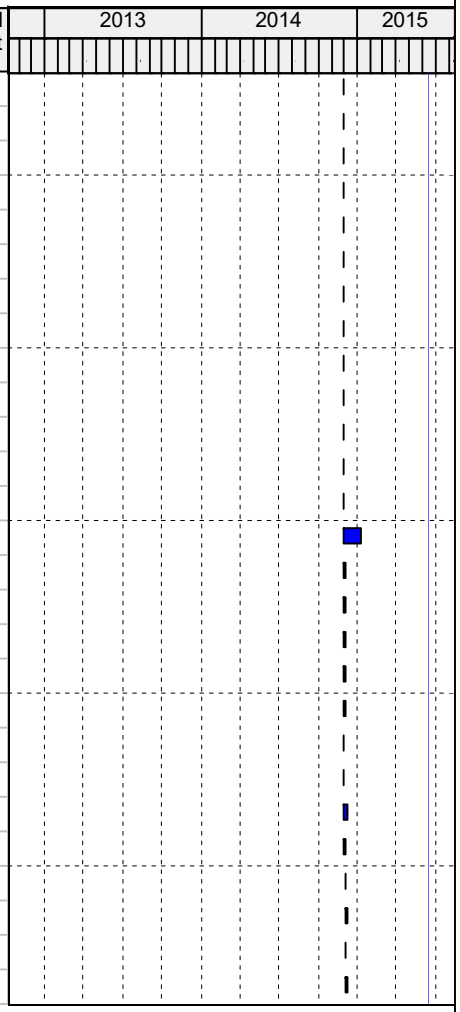



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2308 | Zone 3 - Install site lighting | 5 | 0 | 03-Dec-14 A | 04-Dec-14 A | |
| L10-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 03-Dec-14 A | 15-Dec-14 A | |
| I-1632 | Manlift finishes - Electrical rough-in & inspect | 2 | 0 | 03-Dec-14 A | 10-Dec-14 A | |
| SW-2028 | Zone 4 - Scan Porte Cochere deck | 2 | 0 | 04-Dec-14 A | 05-Dec-14 A | |
| I-1624 | Manlift finishes - Install batt insulation & inspect | 2 | 0 | 04-Dec-14 A | 04-Dec-14 A | |
| I-1626 | Manlift finishes - Shim window openings | 2 | 0 | 04-Dec-14 A | 05-Dec-14 A | |
| I-1628 | Manlift finishes - Install vapor barrier & inspect | 2 | 0 | 04-Dec-14 A | 08-Dec-14 A | |
| I-5054 | RFI 832.1 - South Elevation Emergency Exit with Side | 1 | 0 | 04-Dec-14 A | 18-Dec-14 A | |
| I-1608 | Tower - Install N/S Wing, S. End at manlift (Elev 32) [I | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1012 | Tower - Install N/S Wing, S. End E. Side Concrete (El | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| PC-4012 | Porte Cochere - Install sheet metal capping[DELETEI | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4046 | Tower Roof - Install sheet metal capping[DELETED S | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4060 | Roof at Manlift - Install corrugated metal panels[DELE | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4062 | Roof at Manlift - Install sheet metal capping[DELETE | 2 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4064 | Pool Green Roof - Install sheet metal capping[DELET | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1040 | Tower - Install N/S Wing, S, End (Elev 30)[DELETED | 7 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| MPT-1044 | Enclosure at manlift - Install sign backing south[DELE | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1612 | Enclosure at manlift - Caulking[DELETED SEE REV M | 8 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1614 | Enclosure at manlift - Install rigid insulation at shear w | 3 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1618 | Enclosure at manlift - Install framing at shear wall[DEI | 5 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| I-1620 | Enclosure at manlift - Install hat channel over framing | 5 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| L03-8656 | L3 Pool - Electrical rough-in at ceiling & inspect | 3 | 0 | 05-Dec-14 A | 19-Dec-14 A | |
| I-5058 | RFI 834 - NE Retaining Wall Design Clarifications | 1 | 0 | 05-Dec-14 A | 23-Dec-14 A | |
| I-5062 | RFI 835 - NW Planter Wall Drainage | 1 | 0 | 05-Dec-14 A | 10-Dec-14 A | |
| L1K-8344 | Set kitchen hoods | 8 | 0 | 06-Dec-14 A | 21-Dec-14 A | |
| L12-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L03-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |

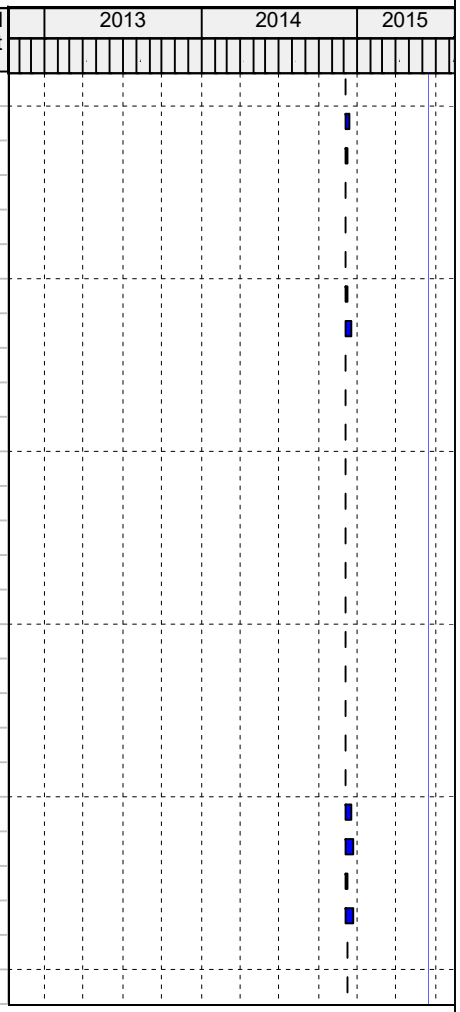



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |
| L05-7030 | Paint | 1 | 0 | 08-Dec-14 A | 08-Dec-14 A | |
| SW-2312 | Zone 3 - Fine grade for sidewalk | 3 | 0 | 08-Dec-14 A | 08-Jan-15 A | |
| RF-4042 | Pool Roof - Install metal coping at high roof | 2 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L17-8130 | Install Door Hardware | 3 | 0 | 08-Dec-14 A | 11-Dec-14 A | |
| L09-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L03-8658 | L3 Pool - Fire sprinkler drops at ceiling & inspect | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| LL2-8140 | LL2 - Install vinyl wall coverings | 2 | 0 | 08-Dec-14 A | 24-Dec-14 A | |
| L04-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L05-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L07-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L08-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L09-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L14-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L15-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 09-Dec-14 A | 12-Dec-14 A | |
| L03-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L07-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L08-7030 | Paint | 1 | 0 | 09-Dec-14 A | 09-Dec-14 A | |
| L04-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L05-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L06-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L07-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L08-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |

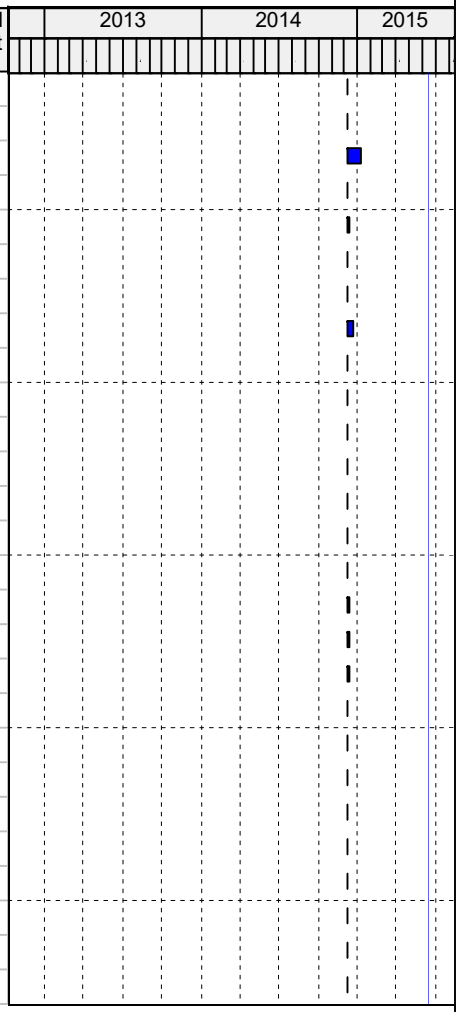



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-7132 | Paint Prime/1st Coat | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| RF-4072 | Pool Roof - Install metal coping | 3 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L17-8204 | Bathrooms - Install Vinyl Wall Covering | 2 | 0 | 09-Dec-14 A | 12-Dec-14 A | |
| L07-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 09-Dec-14 A | 29-Dec-14 A | |
| L06-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 09-Dec-14 A | 24-Dec-14 A | |
| I-1604 | Manlift finishes - GWB, hang walls | 2 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L07-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L08-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 16-Dec-14 A | |
| L11-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L12-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L14-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L15-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L16-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L17-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| LL2E-8340 | LL2 - Install walk-in cooler/freezer (BY OTHERS) | 5 | 0 | 10-Dec-14 A | 15-Dec-14 A | |
| L10-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 10-Dec-14 A | 17-Dec-14 A | |
| L09-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L10-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L11-7030 | Paint | 1 | 0 | 10-Dec-14 A | 10-Dec-14 A | |
| L11-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L12-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L14-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L15-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L16-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L17-7132 | Paint Prime/1st Coat | 3 | 0 | 10-Dec-14 A | 11-Dec-14 A | |
| L08-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 10-Dec-14 A | 29-Dec-14 A | |

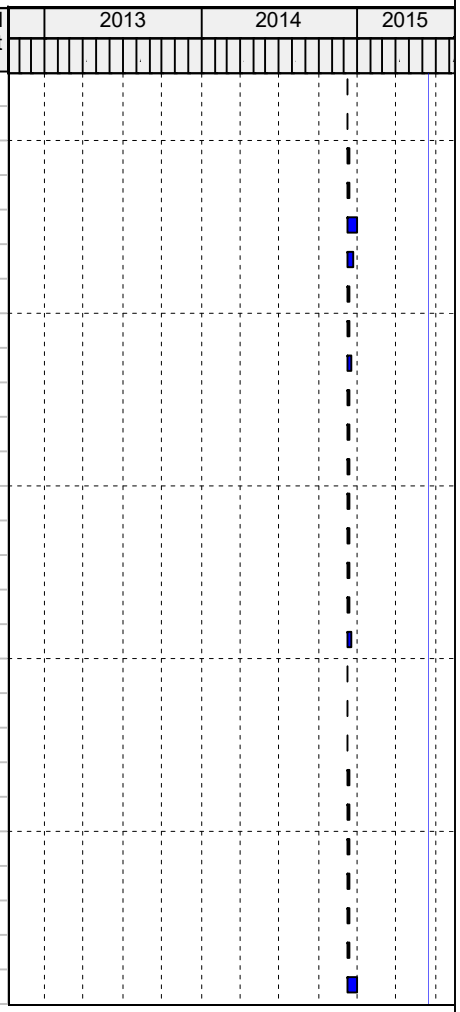



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1634 | Manlift finishes - GWB, hang ceilings | 2 | 0 | 10-Dec-14 A | 16-Dec-14 A | |
| L12-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L14-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L15-7030 | Paint | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L03-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L04-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| MPT-1034 | (A) Elevation 52 (west elevation, north end, L3-L18) | 4 | 0 | 11-Dec-14 A | 16-Dec-14 A | |
| MPT-1036 | (B) Elevation 45/46 (north elevation, east end, L3-L1 | 5 | 0 | 11-Dec-14 A | 19-Dec-14 A | |
| L16-7030 | Paint | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L17-7030 | Paint | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L05-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L06-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| MPT-1066 | Tower Sign, East (El. 32) - Install backing | 3 | 0 | 12-Dec-14 A | 22-Dec-14 A | |
| MPT-1076 | (B) Caulking - Elevation 51 (north elevation, west half | 10 | 0 | 12-Dec-14 A | 19-Dec-14 A | |
| L04-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L04-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L07-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L08-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L09-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L14-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L15-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L17-8201 | Corridors - Install ACT Grid | 2 | 0 | 15-Dec-14 A | 16-Dec-14 A | |
| L04-7042 | Install Tile Flooring (x41) | 2 | 0 | 15-Dec-14 A | 24-Dec-14 A | |

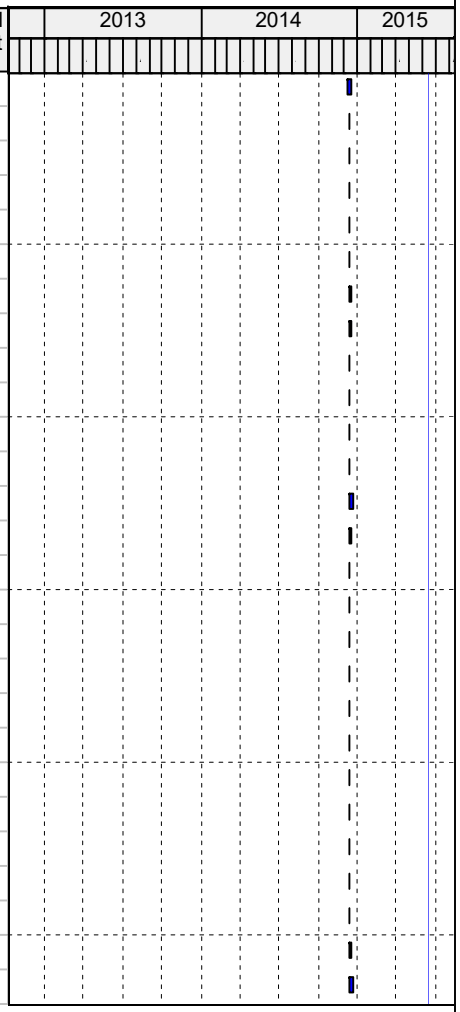



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-7042 | Install Tile Flooring (x41) | 2 | 0 | 15-Dec-14 A | 24-Dec-14 A | |
| LL4-8102a | LL4 - GWB Tape/Finish | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| LL3-8102a | LL3 - GWB Tape/Finish | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| L03-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L04-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L05-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L06-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L07-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L08-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L09-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| L10-7144 | Fire Sprinkler Trim | 1 | 0 | 15-Dec-14 A | 15-Dec-14 A | |
| CO-7126 | Fire pump test pre-planning complete (see checklist) | 0 | 0 | | 15-Dec-14 A | |
| LL1-Z3-6034 | COB Correction - Add ceiling access panels in Food F | 10 | 0 | 15-Dec-14 A | 26-Jan-15 A | |
| L03-8406 | Paint Prime/1st Coat at Elevator Lobby | 3 | 0 | 15-Dec-14 A | 17-Dec-14 A | |
| L05-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L09-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L10-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L10-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L11-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L11-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L14-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L15-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L16-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L17-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| LL2E-8342 | LL2 - Final connections at walk-in cooler/freezer | 5 | 0 | 16-Dec-14 A | 05-Jan-15 A | |

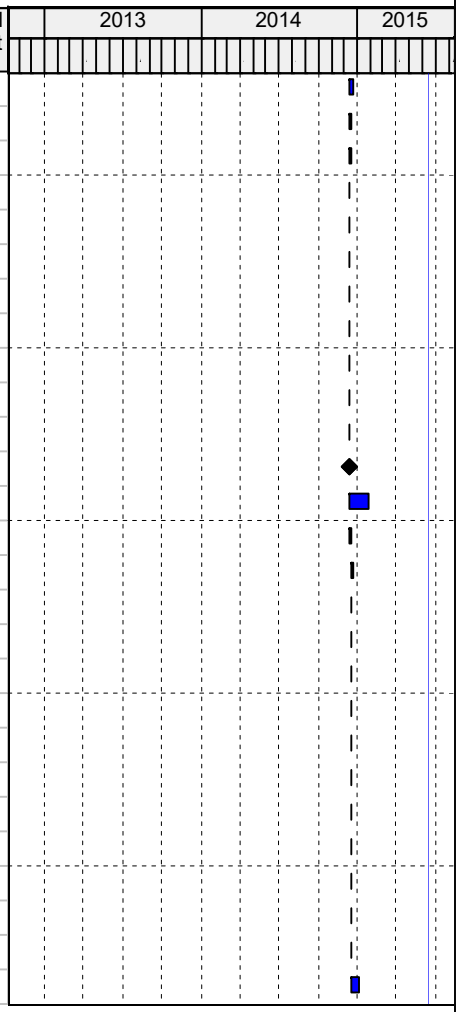


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 16-Dec-14 A | 18-Dec-14 A | |
| L16-8201 | Corridors - Install ACT Grid | 2 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L06-7042 | Install Tile Flooring (x41) | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L07-7042 | Install Tile Flooring (x41) | 2 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| LL1-Z2-8102a | GWB Hang (Ceilings) & Inspection | 3 | 0 | 16-Dec-14 A | 24-Dec-14 A | |
| L11-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L12-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L14-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L15-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L16-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| L17-7144 | Fire Sprinkler Trim | 1 | 0 | 16-Dec-14 A | 16-Dec-14 A | |
| CO-7128 | Run fire pump test | 2 | 0 | 16-Dec-14 A | 17-Dec-14 A | |
| L09-8203 | Corridors - Install Vinyl Wall Coverings | 2 | 0 | 16-Dec-14 A | 30-Dec-14 A | |
| SW-2026 | Zone 4 - FRP NW planter | 5 | 0 | 16-Dec-14 A | 05-Jan-15 A | |
| I-5370 | (S) Resolve south tower sign backing (RFI 844) | 5 | 0 | 16-Dec-14 A | 09-Jan-15 A | |
| L03-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 22-Dec-14 A | |
| L04-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 23-Dec-14 A | |
| L06-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 29-Dec-14 A | |
| L07-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 30-Dec-14 A | |
| L08-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 31-Dec-14 A | |
| L09-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 17-Dec-14 A | 05-Jan-15 A | |
| L14-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L15-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L16-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L17-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L08-7042 | Install Tile Flooring (x41) | 2 | 0 | 17-Dec-14 A | 24-Dec-14 A | |
| L09-7042 | Install Tile Flooring (x41) | 2 | 0 | 17-Dec-14 A | 24-Dec-14 A | |

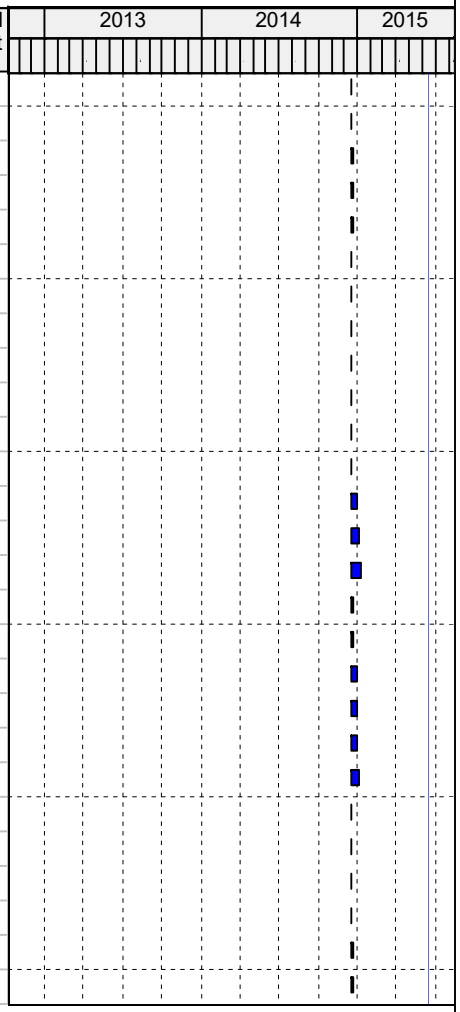



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7136 | Install Door and Hardware | 1 | 0 | 17-Dec-14 A | 17-Dec-14 A | |
| L16-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 17-Dec-14 A | 29-Dec-14 A | |
| MPT-1046 | (A) Elevation 26/27/53 (west elevation, south of 52, L | 3 | 0 | 17-Dec-14 A | 18-Dec-14 A | |
| MPT-1057 | (S) Elevation 32 framing (south elevation, east of mai | 5 | 0 | 17-Dec-14 A | 19-Jan-15 A | |
| MPT-1080 | (A) Caulking - Elevation 44 (east elevation above poo | 8 | 0 | 17-Dec-14 A | 22-Dec-14 A | |
| LL1-Z2-8108 | Framing, ceiling clouds (incl. inspection) | 5 | 0 | 17-Dec-14 A | 22-Jan-15 A | |
| MPP-1006 | (C) Install Level 3 cornice metal (north, west & south) | 6 | 0 | 18-Dec-14 A | 30-Jan-15 A | |
| L10-7042 | Install Tile Flooring (x41) | 2 | 0 | 18-Dec-14 A | 24-Dec-14 A | |
| L11-7042 | Install Tile Flooring (x41) | 2 | 0 | 18-Dec-14 A | 24-Dec-14 A | |
| L12-7042 | Install Tile Flooring (x41) | 2 | 0 | 19-Dec-14 A | 24-Dec-14 A | |
| L14-7042 | Install Tile Flooring (x41) | 2 | 0 | 19-Dec-14 A | 24-Dec-14 A | |
| MPT-1048 | (B) Elevation 37 (penthouse east) | 3 | 0 | 19-Dec-14 A | 20-Dec-14 A | |
| I-5000 | Resolve RFI's and site work changes (new drawings) | 10 | 0 | 19-Dec-14 A | 02-Mar-15 A | |
| I-5002 | Resolve RFI's and site work changes (new drawings) | 20 | 0 | 19-Dec-14 A | 09-Feb-15 A | |
| I-5003 | Resolve RFI's and site work changes (new drawings) | 10 | 0 | 19-Dec-14 A | 02-Mar-15 A | |
| I-5004 | Resolve RFI's and site work changes (new drawings) | 1 | 0 | 19-Dec-14 A | 16-Jan-15 A | |
| I-5064 | RFI 848 - Lighting at Flagpole Locations | 1 | 0 | 19-Dec-14 A | 14-Jan-15 A | |
| L03-8416 | Fire Sprinkler Trim / Finish at Elevator Lobby | 1 | 0 | 22-Dec-14 A | 22-Dec-14 A | |
| L07-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L17-8136 | Bathrooms - Install Counter Subtops | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| CO-7212 | Cx - Start-Up Boilers | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L17-8218 | Corridors - Fire Sprinkler Trim | 2 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L08-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L07-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L06-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L05-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| L04-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 22-Dec-14 A | 22-Dec-14 A | |

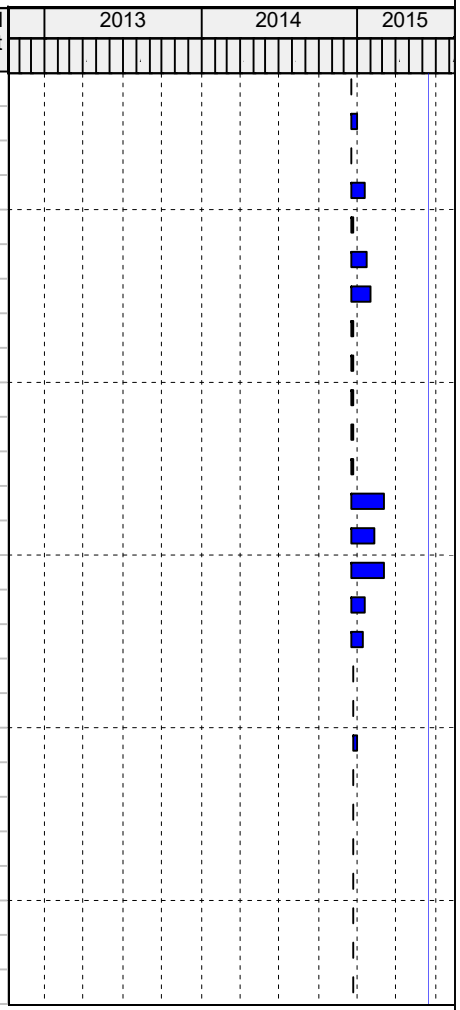



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-1636 | Manlift finishes - GWB, tape & finish | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| EL-6038 | Elev 6 - Rough-in call boxes & lanterns | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| EL-6052 | Elev 6 - Complete hoistway ventilation | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| MPT-1078 | (C) Caulking - Elevation 37/38/39 (penthouse) | 4 | 0 | 22-Dec-14 A | 23-Dec-14 A | |
| MPT-1086 | (A) Caulking - Elevation 45/46 (north elevation, east e | 7 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| MPT-1088 | (B) Caulking - Elevation 52/53/26/27 (west elevation, | 11 | 0 | 22-Dec-14 A | 02-Jan-15 A | |
| MPP-1044 | Caulking - Elevation 9/10/11/12/13 (upper ballroom) | 5 | 0 | 22-Dec-14 A | 30-Dec-14 A | |
| MPP-1046 | Caulking - Elevation 5/6 (east elevation, south end) | 8 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| I-5068 | RFI 857 - South Elevation Landscape & Irrigation Rec | 1 | 0 | 22-Dec-14 A | 07-Jan-15 A | |
| I-5070 | RFI 858 - North Elevation Landscape & Irrigation Req | 1 | 0 | 22-Dec-14 A | 07-Jan-15 A | |
| I-5072 | RFI 859 - Additional Curbs at Openings (see RFI 776) | 1 | 0 | 22-Dec-14 A | 07-Jan-15 A | |
| L03-8414 | Elec Trim / Finish at Elevator Lobby | 3 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L03-7032 | Install VCT Flooring (x42) | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L08-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L10-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| L09-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 23-Dec-14 A | 24-Dec-14 A | |
| ASI62 | ASI No. 62 - Civil Site Grading Revisions | 0 | 0 | 23-Dec-14 A | | |
| I-5074 | RFI 860 - SE Corner Hardscape Additional Clarificatio | 1 | 0 | 23-Dec-14 A | 07-Jan-15 A | |
| L09-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 24-Dec-14 A | 29-Dec-14 A | |
| L03-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 31-Dec-14 A | |
| L15-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L16-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L17-7042 | Install Tile Flooring (x41) | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L04-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L05-7136 | Install Door and Hardware | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L10-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L17-8216 | Vinyl Wall Coverings - Install Murals | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |

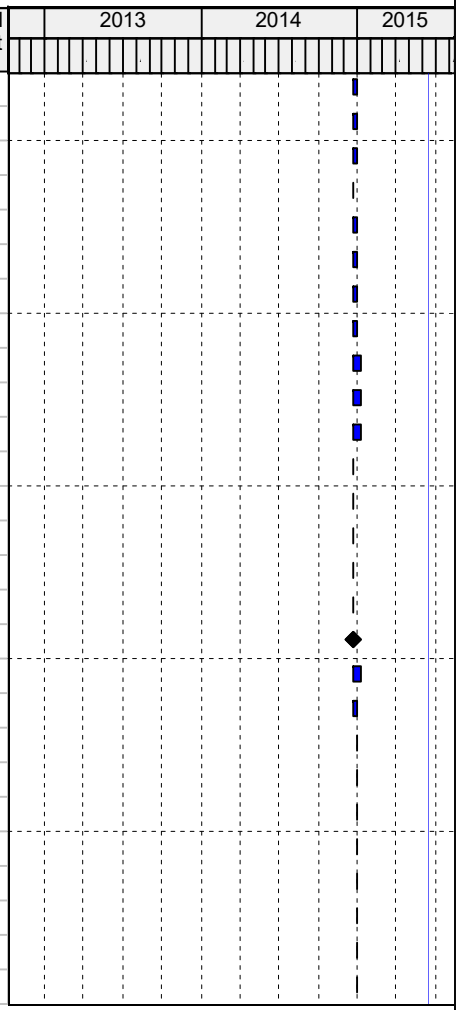



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-8202 | Install FRP wall coverings | 4 | 0 | 29-Dec-14 A | 06-Jan-15 A | |
| L04-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L05-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L06-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| L07-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L08-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L09-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L10-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL2-8130 | LL2 - Install ceiling grid | 2 | 0 | 29-Dec-14 A | 30-Dec-14 A | |
| I-5300 | Heat Pump Revision - demo existing ceiling framing | 2 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| L12-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 30-Dec-14 A | 05-Jan-15 A | |
| L06-7136 | Install Door and Hardware | 1 | 0 | 30-Dec-14 A | 30-Dec-14 A | |
| L11-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 30-Dec-14 A | 31-Dec-14 A | |
| I-5302 | Heat Pump Revision - rework MEP at celing | 5 | 0 | 30-Dec-14 A | 12-Jan-15 A | |
| I-1606 | Manlift finishes - Prime & paint | 4 | 0 | 31-Dec-14 A | 06-Jan-15 A | |
| L07-7136 | Install Door and Hardware | 1 | 0 | 31-Dec-14 A | 31-Dec-14 A | |
| L12-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 31-Dec-14 A | 05-Jan-15 A | |
| CO-7214 | Cx - Flush & Fill HVAC Hydronics Systems | 5 | 0 | 02-Jan-15 A | 05-Jan-15 A | |
| MPP-1032 | (C) Elevation 23/24/25 (Porte Cochere north, below c | 5 | 0 | 02-Jan-15 A | 19-Jan-15 A | |
| L1BOH2-8215 | GWB tape & finish walls & ceilings | 7 | 0 | 05-Jan-15 A | 02-Mar-15 A | |
| L10-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| L11-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 13-Jan-15 A | |
| L12-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 05-Jan-15 A | 13-Jan-15 A | |
| L14-8129 | Bathrooms - Install Shower Doors | 4 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| L16-8121 | Install Bathroom "Barn Doors" | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L04-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L05-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |

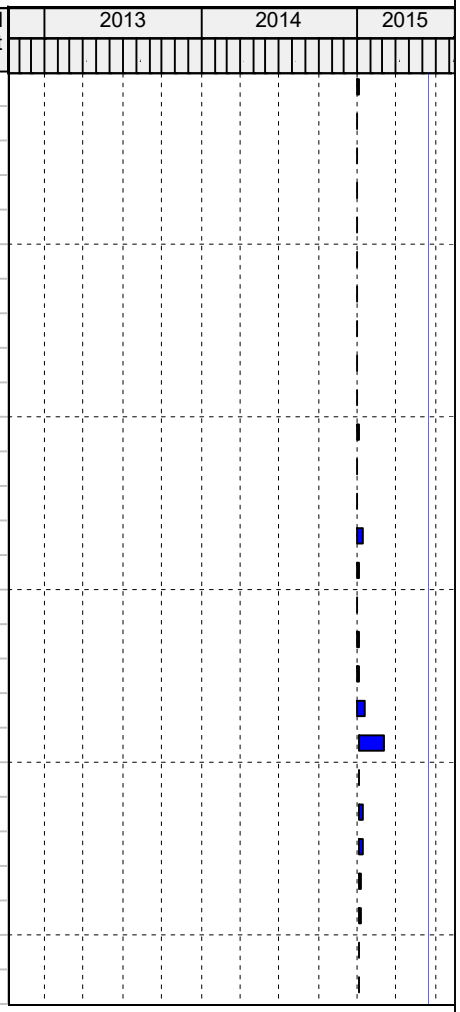



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-7032 | Install VCT Flooring (x42) | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L05-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| L06-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L07-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L08-7136 | Install Door and Hardware | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L08-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L09-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L10-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 05-Jan-15 A | 05-Jan-15 A | |
| L14-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| SW-2314 | Zone 3 - FRP sidewalk | 5 | 0 | 05-Jan-15 A | 16-Feb-15 A | |
| L10-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 05-Jan-15 A | 27-Jan-15 A | |
| CO-7240 | Cx - Heat Pump Start-Up - Levels 3 & 4 | 5 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| SW-2220 | Zone 2 - FRP curb/gutter at NW corner | 4 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| MPT-1054 | Complete Elevation 30 (south elevation, west of man | 5 | 0 | 05-Jan-15 A | 18-Mar-15 A | |
| MPP-1028 | (C) Tapered pilasters, west | 3 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| MPP-1030 | (C) Tapered pilasters, east | 3 | 0 | 05-Jan-15 A | 06-Jan-15 A | |
| LL2-8142 | HVAC drops/trim to grid | 3 | 0 | 05-Jan-15 A | 19-Jan-15 A | |
| L1L-8216 | Complete electrical/fire alarm drops @ ceilings | 5 | 0 | 05-Jan-15 A | 08-Jan-15 A | |
| L1BOH2-8217 | GWB hang ceilings and at heat pumps | 10 | 0 | 05-Jan-15 A | 29-Jan-15 A | |
| L1L-8222 | Complete HVAC drops @ ceilings | 5 | 0 | 05-Jan-15 A | 23-Jan-15 A | |
| L1L-8224 | Complete fire sprinkler drops @ ceilings | 5 | 0 | 05-Jan-15 A | 08-Jan-15 A | |
| L1L-8254 | Complete electrical rough-in at walls | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| I-5350 | Fabricate & install new hydraulic ram | 30 | 0 | 05-Jan-15 A | 29-Jan-15 A | |
| I-7800 | Procure light poles and replacement luminaires | 40 | 0 | 05-Jan-15 A | 12-Jun-15 A | |
| LL1-8120 | Complete GWB tape & finish in corridors | 7 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| L1K-8108 | Complete kitchen hood installation and fire blanket w | 10 | 0 | 05-Jan-15 A | 05-Feb-15 A | |
| L1K-8110 | Complete MEP rough-in above ceiling | 10 | 0 | 05-Jan-15 A | 05-Feb-15 A | |

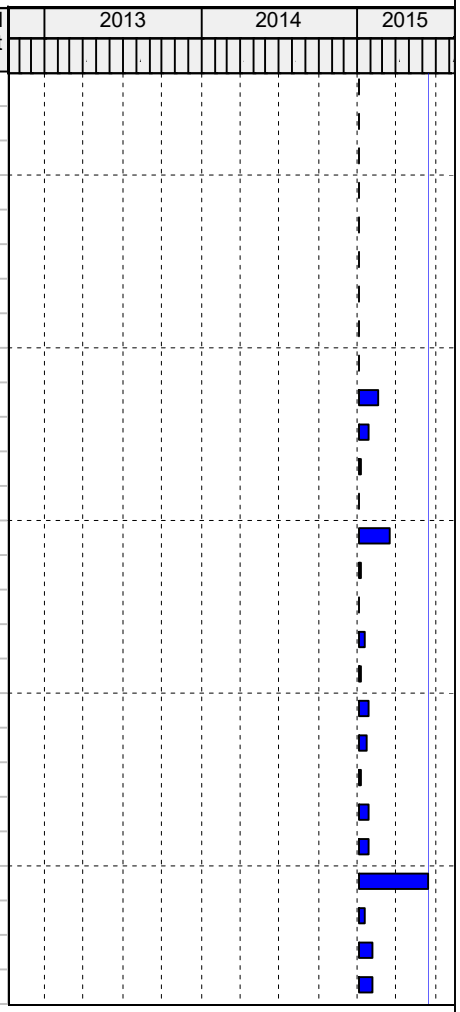



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-8122 | Framing, complete ceiling at corridors | 5 | 0 | 05-Jan-15 A | 13-Jan-15 A | |
| I-5102 | Bar lighting layout - resolve conflicts (RFI) | 7 | 0 | 05-Jan-15 A | 19-Jan-15 A | |
| I-5110 | Bar radius ceiling - resolve framing issues | 5 | 0 | 05-Jan-15 A | 14-Jan-15 A | |
| I-5120 | Dining feature wall - resolve design issues | 7 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| L02-8178 | Complete heat pump enclosures | 5 | 0 | 05-Jan-15 A | 12-Jan-15 A | |
| I-5850 | Owner provide revised lighting layout | 10 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| I-5130 | Bar plumbing relocation - resolve conflicts | 25 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| I-5140 | Damper at BPF #8 - resolve conflicts | 30 | 0 | 05-Jan-15 A | 29-Jan-15 A | |
| I-5150 | Sprinkler pipe furring - resolve conflicts | 15 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| I-5160 | ASI 63 electrical revisions - resolve conflicts | 10 | 0 | 05-Jan-15 A | 16-Jan-15 A | |
| L15-8410 | Vinyl Wall Coverings at Elevator Lobby | 2 | 0 | 06-Jan-15 A | 07-Jan-15 A | |
| L07-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L08-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L09-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L10-7032 | Install VCT Flooring (x42) | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L09-7136 | Install Door and Hardware | 1 | 0 | 06-Jan-15 A | 06-Jan-15 A | |
| L10-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L11-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L12-7136 | Install doors & hardware | 1 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L15-8138 | Bathrooms - Install Toilet Accessories | 2 | 0 | 06-Jan-15 A | 07-Jan-15 A | |
| L11-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 06-Jan-15 A | 12-Jan-15 A | |
| L03-8660 | GWB hang ceilings at Pool | 3 | 0 | 06-Jan-15 A | 04-Feb-15 A | |
| L1K-6011 | Complete HVAC RI @ ceilings | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L1K-6013 | Complete electrical rough-in @ ceilings & inspection | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L1K-6015 | Complete fire sprinkler RI @ ceilings | 4 | 0 | 06-Jan-15 A | 13-Jan-15 A | |
| L12-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L14-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |

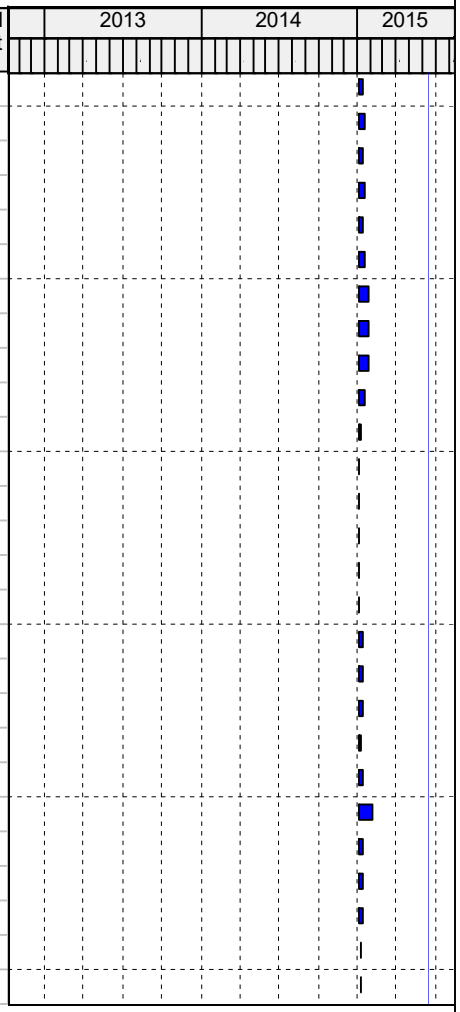



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L16-7032 | Install VCT Flooring (x42) | 1 | 0 | 07-Jan-15 A | 07-Jan-15 A | |
| L15-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 07-Jan-15 A | 20-Jan-15 A | |
| L12-8203 | Wall coverings - vinyl at corridors | 2 | 0 | 07-Jan-15 A | 13-Jan-15 A | |
| CO-7242 | Cx - Heat Pump Start-Up - Levels 5 & 6 | 5 | 0 | 07-Jan-15 A | 09-Jan-15 A | |
| CO-7252 | Cx - Start-Up - FSD & SD Operation Verification | 10 | 0 | 07-Jan-15 A | 22-Jan-15 A | |
| MPP-1026 | Complete Elevation 7/8 (east elevation) | 5 | 0 | 07-Jan-15 A | 16-Feb-15 A | |
| ASI61 | ASI No. 61 - VHP-1 Ductwork Change at Elevator 5 L | 0 | 0 | 07-Jan-15 A | | |
| I-5056 | RFI 832.1 - South Elevation Emergency Exit with Side | 1 | 0 | 07-Jan-15 A | 14-Jan-15 A | |
| LL1-6014Ib2 | L1 bar redesign - GWB hang, tape, finish (including ir | 12 | 0 | 08-Jan-15 A | 30-Jan-15 A | |
| SW-2310 | Zone 3 - Install irrigation sleeves | 2 | 0 | 08-Jan-15 A | 08-Jan-15 A | |
| I-1638 | Manlift finishes - ceiling grid | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| L03-8662 | GWB tape & finish walls & ceilings at Pool | 7 | 0 | 08-Jan-15 A | 25-Feb-15 A | |
| MPT-1072 | Tower Sign, West (El, 52) | 5 | 0 | 08-Jan-15 A | 14-Apr-15 A | |
| L1L-8220 | Complete fire sprinkler RI @ ceilings | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| L1L-8270 | Complete HVAC RI @ ceilings | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| SW-2224 | Zone 2 - Adjust Comcast vault lids | 2 | 0 | 08-Jan-15 A | 08-Jan-15 A | |
| I-1212 | Resolve stud/duct conflict at east wall | 5 | 0 | 08-Jan-15 A | 14-Jan-15 A | |
| L04-8218 | Install base at corridors (& approve mockup) | 3 | 0 | 08-Jan-15 A | 12-Jan-15 A | |
| GB410-100 | Complete GWB - Levels 4-10 | 5 | 0 | 08-Jan-15 A | 14-Jan-15 A | |
| LL1-6014Ib4 | L1 bar redesign - complete reframing | 5 | 0 | 08-Jan-15 A | 15-Jan-15 A | |
| I-5306 | Heat Pump Revision - complete reframing | 5 | 0 | 08-Jan-15 A | 19-Jan-15 A | |
| ASI63 | ASI No. 63 - Mech (Rev. 20), Plumbing (Rev. 18) and | 0 | 0 | 09-Jan-15 A | | |
| L15-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L16-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8129 | Bathrooms - Install shower doors | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8121 | Install Bathroom "Barn Doors" | 3 | 0 | 12-Jan-15 A | 26-Mar-15 A | |

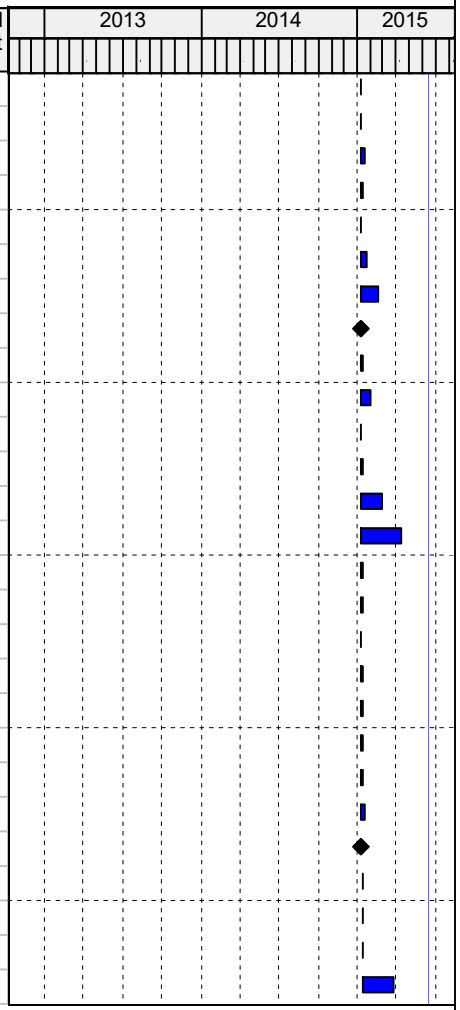


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L05-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L06-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L07-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L08-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L09-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L10-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L11-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L12-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L14-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L15-7034 | Install doors & hardware (x42) | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L11-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L14-7136 | Install doors & hardware | 1 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| L14-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L15-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L15-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L14-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L11-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L03-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 12-Jan-15 A | 19-Jan-15 A | |
| CO-7244 | Cx - Heat Pump Start-Up - Levels 7 & 8 | 5 | 0 | 12-Jan-15 A | 14-Jan-15 A | |
| MPT-1068 | Tower Sign, North (El. 51) | 5 | 0 | 12-Jan-15 A | 10-Mar-15 A | |
| L03-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L11-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L12-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L14-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |

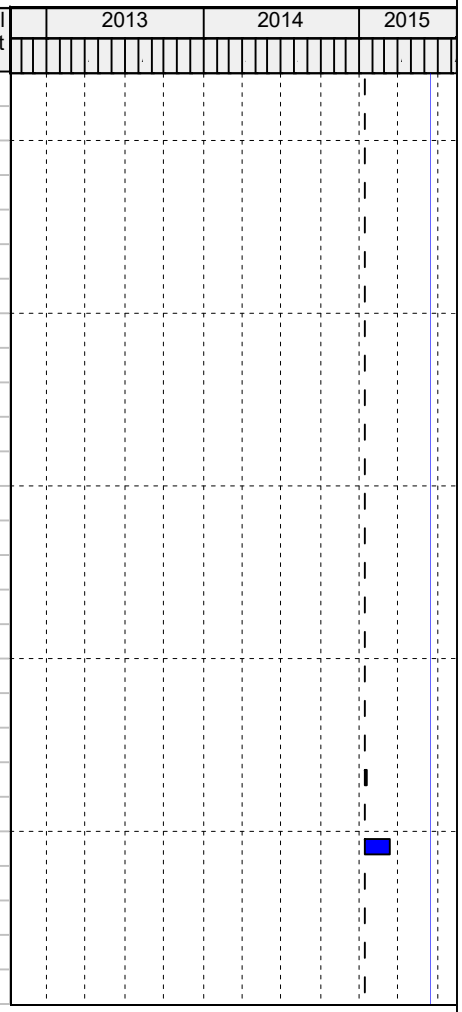



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| L02-8144 | GWB hang at Locker Rooms | 2 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| SW-2326 | Zone 3 - Install j-boxes | 3 | 0 | 12-Jan-15 A | 12-Jan-15 A | |
| I-5800 | Mechanical correction notice - interference with light t | 10 | 0 | 12-Jan-15 A | 13-Feb-15 A | |
| I-5602 | Frame FCC ceiling | 2 | 0 | 12-Jan-15 A | 13-Jan-15 A | |
| CO-7166 | Replace exhaust fitting | 10 | 0 | 12-Jan-15 A | 28-Jan-15 A | |
| MPP-1034 | Deliver Elevation 48 corner panels | 25 | 0 | 12-Jan-15 A | 27-Feb-15 A | |
| MPP-1042 | Deliver Elevation 32 corner panels | 25 | 0 | 12-Jan-15 A | 02-Feb-15 A | |
| MPP-1066 | Deliver Elevation 33/34 corner panels | 25 | 0 | 12-Jan-15 A | 27-Feb-15 A | |
| MPP-1068 | Deliver Elevation 32 spandrel panel head/sill flashings | 25 | 0 | 12-Jan-15 A | 13-Feb-15 A | |
| MPP-1070 | Deliver Elevation 44 spandrel panel head/sill flashings | 25 | 0 | 12-Jan-15 A | 13-Feb-15 A | |
| MPP-1072 | Deliver remaining Elevation 4 panels | 25 | 0 | 12-Jan-15 A | 06-Feb-15 A | |
| MPP-1074 | Deliver remaining Elevation 7 panels | 25 | 0 | 12-Jan-15 A | 06-Feb-15 A | |
| MPP-1076 | Deliver Pool cornice panels | 25 | 0 | 12-Jan-15 A | 23-Mar-15 A | |
| ASI64 | ASI No. 64 - Updated Public Space Carpet Specificat | 0 | 0 | 12-Jan-15 A | | |
| L15-7136 | Install doors & hardware | 1 | 0 | 13-Jan-15 A | 16-Feb-15 A | |
| L03-8664 | Paint, prime & first coat finish at Pool | 3 | 0 | 13-Jan-15 A | 23-Mar-15 A | |
| MPP-1022 | (A) Complete Elevation 40 (pool south elevation, L3-L | 5 | 0 | 13-Jan-15 A | 20-Jan-15 A | |
| L05-8226 | Install base at corridors | 1 | 0 | 13-Jan-15 A | 13-Jan-15 A | |
| L16-8138 | Bathrooms - Install toilet accessories | 2 | 0 | 14-Jan-15 A | 15-Jan-15 A | |
| L14-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| CO-7246 | Cx - Heat Pump Start-Up - Levels 9 & 10 | 5 | 0 | 14-Jan-15 A | 16-Jan-15 A | |
| I-5604 | GWB hang, tape & finish FCC ceiling | 5 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| I-5076 | RFI 860.1 - Southeast Elevation Conflict | 1 | 0 | 14-Jan-15 A | 17-Mar-15 A | |
| I-5078 | RFI 884 - Pedestrian Light Pole Base and Drain Conf | 1 | 0 | 14-Jan-15 A | 28-Jan-15 A | |
| L14-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 15-Jan-15 A | 16-Jan-15 A | |
| L16-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 15-Jan-15 A | 21-Jan-15 A | |

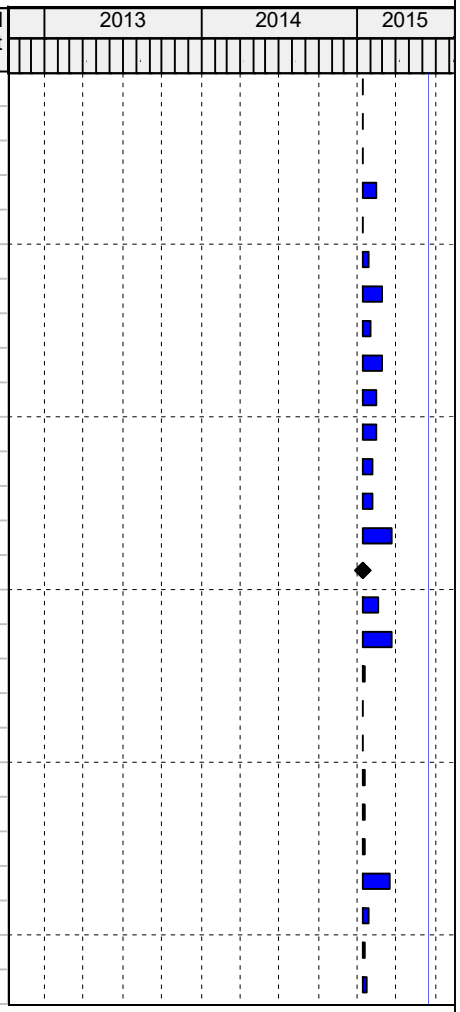


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2126 | Zone 1 - Remove temporary transformer | 5 | 0 | 15-Jan-15 A | 28-Jan-15 A | |
| I-5112 | Bar radius ceiling - complete framing | 5 | 0 | 15-Jan-15 A | 20-Jan-15 A | |
| I-5080 | RFI 889 - Site Channelization Plan | 1 | 0 | 15-Jan-15 A | 11-Mar-15 A | |
| L07-8226 | Install base at corridors | 1 | 0 | 16-Jan-15 A | 16-Jan-15 A | |
| I-5060 | RFI 834.1 - NE Retaining Wall Design Clarifications - ( | 1 | 0 | 16-Jan-15 A | 02-Feb-15 A | |
| L16-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| CO-7248 | Cx - Heat Pump Start-Up - Levels 11 & 12 | 5 | 0 | 19-Jan-15 A | 21-Jan-15 A | |
| CO-7254 | Cx - Start-Up - MUA AAON (8) | 5 | 0 | 19-Jan-15 A | 20-Feb-15 A | |
| SW-2020 | Porte Cochere - EIFS at ceiling | 7 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L02-8146 | GWB tape & finish at Locker Rooms | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L1K-8138 | Complete GWB hang & tape | 9 | 0 | 19-Jan-15 A | 06-Feb-15 A | |
| L1L-8252 | Complete electrical/fire alarm rough-in @ ceilings | 3 | 0 | 19-Jan-15 A | 26-Jan-15 A | |
| LL1-8122 | Paint corridors | 6 | 0 | 19-Jan-15 A | 21-Jan-15 A | |
| L1B-6027 | Framing, ceiling at East Ballroom | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L09-8226 | Install base at corridors | 1 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| GB410-102 | Complete painting - Levels 4-10 | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL1-Z2-8110 | Paint, prime & first coat finish at Meeting Rooms | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| I-5122 | Dining feature wall - complete framing | 3 | 0 | 19-Jan-15 A | 21-Jan-15 A | |
| I-5162 | ASI 63 electrical revisions - demo existing | 1 | 0 | 19-Jan-15 A | 19-Jan-15 A | |
| L1B-8170 | Complete cover inspections | 5 | 0 | 19-Jan-15 A | 23-Jan-15 A | |
| L17-8138 | Bathrooms - Install toilet accessories | 2 | 0 | 20-Jan-15 A | 31-Mar-15 A | |
| MPP-1014 | Caulking - Elevation 1/2/A/B/C/23/24/25 (west elevati | 9 | 0 | 20-Jan-15 A | 30-Jan-15 A | |
| CO-7232 | Cx - TAB - CW Pump Totalization | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| L03-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| LL1-8202 | HVAC trim at ceiling | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| LL1-8206 | Lighting & electrical trim | 4 | 0 | 20-Jan-15 A | 28-Jan-15 A | |
| LL1-8208 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 20-Jan-15 A | 21-Jan-15 A | |

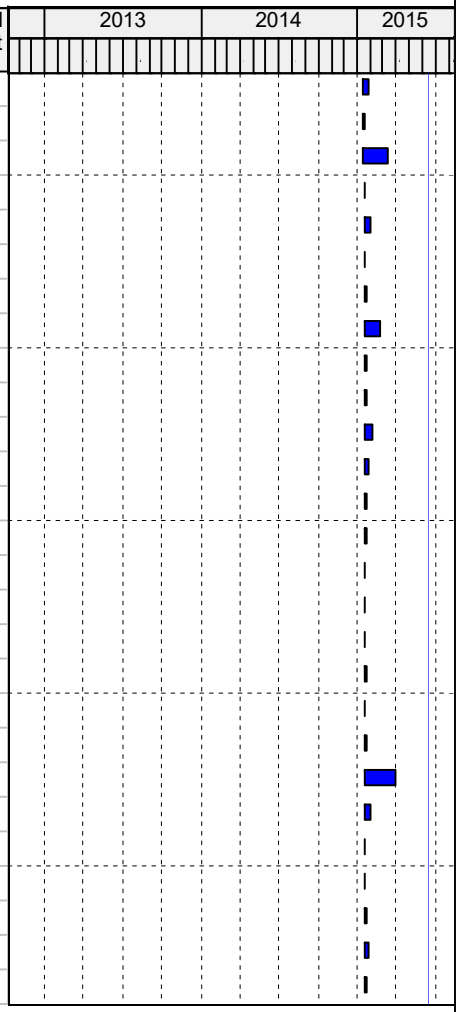



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-8138 | Paint corridors | 3 | 0 | 20-Jan-15 A | 04-Feb-15 A | |
| L10-8226 | Install base at corridors | 1 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| GB410-106 | Complete flooring - Levels 4-10 | 3 | 0 | 20-Jan-15 A | 26-Jan-15 A | |
| L04-8422 | Floor prep | 1 | 0 | 20-Jan-15 A | 02-Feb-15 A | |
| I-5606 | Paint FCC ceiling | 1 | 0 | 20-Jan-15 A | 20-Jan-15 A | |
| I-5104 | Bar lighting layout - complete elecrical rough-in | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| I-5164 | ASI 63 electrical revisions - revise electrical | 3 | 0 | 20-Jan-15 A | 02-Feb-15 A | |
| L16-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| CO-7234 | Cx - TAB - CW Water Balancing | 10 | 0 | 21-Jan-15 A | 06-Mar-15 A | |
| L15-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L14-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L12-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L11-8140 | Install window sills | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L16-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| CO-7250 | Cx - Heat Pump Start-Up - Levels 14 & 15 | 5 | 0 | 21-Jan-15 A | 23-Jan-15 A | |
| L16-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| I-5304 | Heat Pump Revision - rework GWB | 9 | 0 | 21-Jan-15 A | 30-Jan-15 A | |
| L03-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L04-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L05-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L06-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L07-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L08-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L09-8131 | Bathrooms - Install access panels | 1 | 0 | 21-Jan-15 A | 21-Jan-15 A | |
| L11-8226 | Install base at corridors | 1 | 0 | 21-Jan-15 A | 22-Jan-15 A | |
| L05-8422 | Floor prep | 1 | 0 | 21-Jan-15 A | 02-Feb-15 A | |
| ASI65 | ASI No. 65 - Framing Revisions at Foyer 101 | 0 | 0 | 21-Jan-15 A | | |

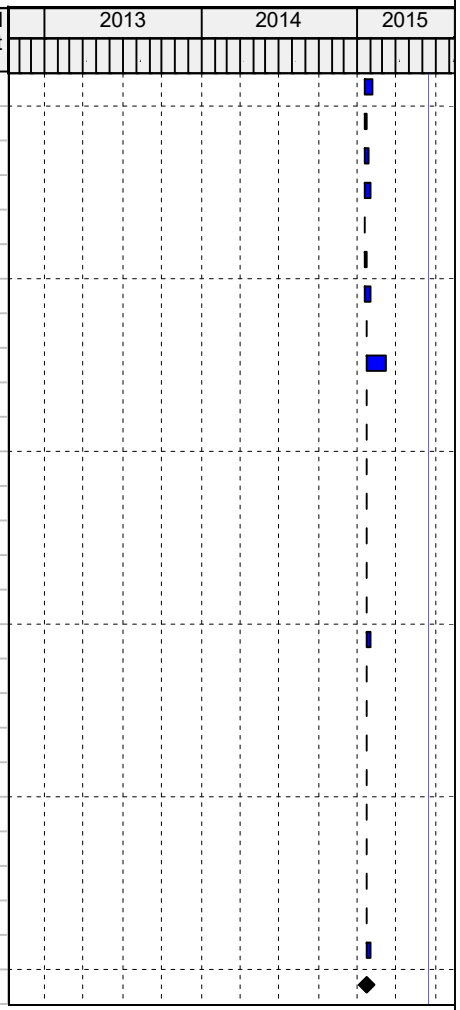



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L07-7134 | Flooring - VCT | 1 | 0 | 22-Jan-15 A | 22-Jan-15 A | |
| L17-8203 | Wall coverings - vinyl at corridors | 3 | 0 | 22-Jan-15 A | 27-Jan-15 A | |
| LL1-8210 | Fire sprinkler trim | 1 | 0 | 22-Jan-15 A | 22-Jan-15 A | |
| L12-8226 | Install base at corridors | 1 | 0 | 22-Jan-15 A | 23-Jan-15 A | |
| L05-7134 | Flooring - VCT | 1 | 0 | 23-Jan-15 A | 23-Jan-15 A | |
| MPP-1016 | Caulking - Elevation 7/8 (east elevation) | 8 | 0 | 23-Jan-15 A | 24-Feb-15 A | |
| LL1-Z2-8120 | GWB hang, tape & finish ceiling clouds at Jr. Ballroon | 7 | 0 | 23-Jan-15 A | 17-Feb-15 A | |
| LL1-Z3-8148 | Paint Restrooms | 3 | 0 | 23-Jan-15 A | 26-Jan-15 A | |
| MPT-1104 | (B) Install alcoves, east (Elev. 7/8) | 2 | 0 | 23-Jan-15 A | 09-Feb-15 A | |
| L06-8422 | Floor prep | 1 | 0 | 23-Jan-15 A | 23-Jan-15 A | |
| L17-8410 | Wall coverings - vinyl at Elevator Lobby | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L06-7134 | Flooring - VCT | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| CO-7216 | Cx - Start-Up Fluid Cooler (power, pre-start & start) | 3 | 0 | 26-Jan-15 A | 28-Jan-15 A | |
| L16-8140 | Install window sills | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| L04-8224 | HVAC grilles & registers at corridors | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| MPT-1058 | Elevation 32 hat channel (south elevation, east of ma | 3 | 0 | 26-Jan-15 A | 17-Feb-15 A | |
| MPT-1090 | Caulking - Elevation 40 (pool south elevation, L3-L17 | 9 | 0 | 26-Jan-15 A | 05-Feb-15 A | |
| LL1-8123 | Floor prep | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| SW-2052 | Zone 4 - Waterproof NW planter walls | 4 | 0 | 26-Jan-15 A | 29-Jan-15 A | |
| L1L-8290 | GWB, top rock | 3 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L10-8131 | Bathrooms - Install access panels | 1 | 0 | 26-Jan-15 A | 26-Jan-15 A | |
| L14-8226 | Install base at corridors | 1 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| I-5372 | (S) Elevation 32, complete insulation | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| GB1117-100 | Complete GWB - Levels 3, 11-16 | 7 | 0 | 26-Jan-15 A | 30-Jan-15 A | |
| SW-2322 | Zone 3 - FRP landscape curb at exit door | 5 | 0 | 26-Jan-15 A | 30-Jan-15 A | |
| I-6010 | RFI 901 - Pool radius trench drain issue | 10 | 5 | 26-Jan-15 A | 19-Jun-15 | 0 |
| L03-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |

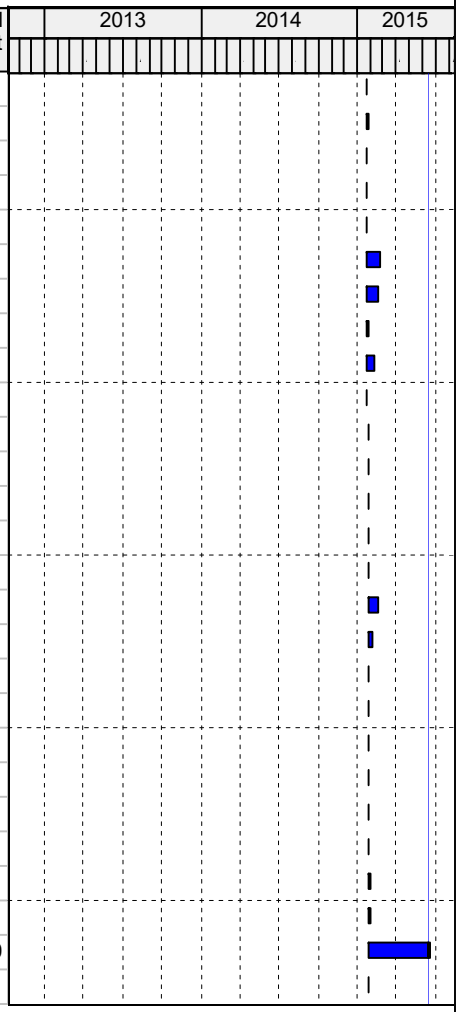


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L16-7034 | Install doors & hardware (x42) | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L17-7034 | Install doors & hardware (x42) | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L08-7134 | Flooring - VCT | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L16-7138 | Electrical trim & finish | 1 | 0 | 27-Jan-15 A | 18-Feb-15 A | |
| L17-7136 | Install doors & hardware | 1 | 0 | 27-Jan-15 A | 17-Feb-15 A | |
| I-1640 | Manlift finishes - Install window sills | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L03-8668 | Remove scaffolding at pool pit | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L17-8420 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L11-8131 | Bathrooms - Install access panels | 1 | 0 | 27-Jan-15 A | 27-Jan-15 A | |
| L15-8226 | Install base at corridors | 1 | 0 | 27-Jan-15 A | 28-Jan-15 A | |
| MPP-1052 | (B) Elevation 3 (south elevation, west of manlift, L1-L: | 5 | 0 | 27-Jan-15 A | 30-Jan-15 A | |
| GB410-108 | Complete base - Levels 4-10 | 4 | 0 | 27-Jan-15 A | 30-Jan-15 A | |
| L08-8422 | Floor prep | 1 | 0 | 27-Jan-15 A | 28-Jan-15 A | |
| I-5132 | Bar plumbing relocation - relocate waste line | 3 | 0 | 27-Jan-15 A | 29-Jan-15 A | |
| I-5152 | Sprinkler pipe furring - install framing around pipe | 2 | 0 | 27-Jan-15 A | 28-Jan-15 A | |
| L09-7134 | Flooring - VCT | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L17-7140 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L17-8222 | Fire alarm trim (speaker/strobe & smoke detector bas | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| EL-6042 | Elev 6 - Install EMR heat pump | 6 | 0 | 28-Jan-15 A | 25-Feb-15 A | |
| MPT-1056 | Complete Elevation 31 (above L12 terrace, west elev | 3 | 0 | 28-Jan-15 A | 13-Feb-15 A | |
| L1L-8256 | GWB hang walls | 3 | 0 | 28-Jan-15 A | 05-Feb-15 A | |
| SW-2230 | Zone 2 - Repair sidewalk north of 3rd Ave | 5 | 0 | 28-Jan-15 A | 30-Jan-15 A | |
| L12-8131 | Bathrooms - Install access panels | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L08-8226 | Install base at corridors | 1 | 0 | 28-Jan-15 A | 30-Jan-15 A | |
| L16-8226 | Install base at corridors | 1 | 0 | 28-Jan-15 A | 29-Jan-15 A | |
| I-5373 | (S) Elevation 32, install sign backing | 1 | 0 | 28-Jan-15 A | 28-Jan-15 A | |
| L07-8422 | Floor prep | 1 | 0 | 28-Jan-15 A | 03-Feb-15 A | |

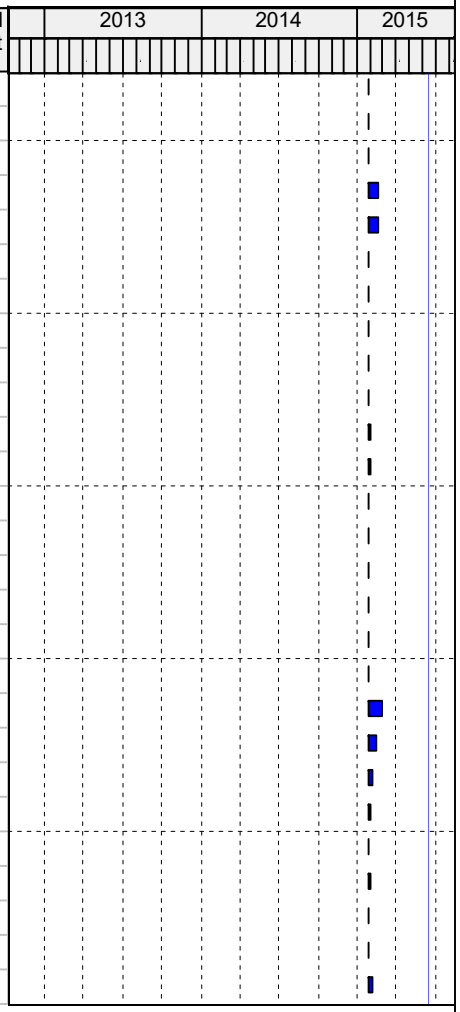



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-6000 | Resolve cloud framing engineering issue | 5 | 0 | 28-Jan-15 A | 03-Feb-15 A | |
| L10-7134 | Flooring - VCT | 1 | 0 | 29-Jan-15 A | 29-Jan-15 A | |
| L1L-8226 | GWB hang ceilings & complete walls | 3 | 0 | 29-Jan-15 A | 23-Feb-15 A | |
| L1L-8248 | Complete electrical/fire alarm rough-in @ ceilings | 3 | 0 | 29-Jan-15 A | 02-Feb-15 A | |
| L1L-8250 | Complete HVAC RI @ ceilings | 5 | 0 | 29-Jan-15 A | 04-Feb-15 A | |
| L03-8218 | Install base at corridors | 1 | 0 | 29-Jan-15 A | 30-Jan-15 A | |
| MPP-1062 | (C) Install level 3 cornice metal (Porte Cochere) | 2 | 0 | 29-Jan-15 A | 04-Feb-15 A | |
| EL-6040 | Elev 6 - Install machine room controller equipment/hy | 3 | 0 | 30-Jan-15 A | 24-Feb-15 A | |
| EL-6054 | Elev 6 - Install EMR doors, hardware & labeling | 2 | 0 | 30-Jan-15 A | 23-Feb-15 A | |
| LL1-8160 | Flooring - carpet | 10 | 0 | 30-Jan-15 A | 18-Feb-15 A | |
| I-5472 | Reframe Laundry Room ceiling (per ceiling height RF | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5474 | Restore Laundry Room GWB (hang & tape) (per ceili | 5 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5476 | Repaint Laundry Room ceiling | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5478 | Demo existing Laundry Room ceiling | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5480 | Revise MEP above Laundry Room ceiling | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5134 | Bar plumbing relocation - adust framing | 1 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5136 | Bar plumbing relocation - GWB hang, tape & finish [D | 7 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5138 | Bar plumbing relocation - paint [DELETED] | 2 | 0 | 30-Jan-15 A | 30-Jan-15 A | |
| I-5142 | Damper at BPF #8 - mechanical revisions | 2 | 0 | 30-Jan-15 A | 02-Feb-15 A | |
| L04-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 02-Feb-15 A | 02-Feb-15 A | |
| L04-7134 | Flooring - VCT | 1 | 0 | 02-Feb-15 A | 02-Feb-15 A | |
| LL1-8124a | Install base | 10 | 0 | 02-Feb-15 A | 23-Feb-15 A | |
| CO-7218 | Cx - Heat Pump Start-Up - Levels 16 & 17 | 5 | 0 | 02-Feb-15 A | 04-Feb-15 A | |
| LL1-6014Id | L1 bar redesign - paint ceilings at Excercise & MR9 | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| EL-1236 | Elev 1&2 - Walsh/TKE pre-inspection | 6 | 0 | 02-Feb-15 A | 27-Feb-15 A | |
| MPT-1050 | (B) Install louvers, east | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| MPT-1070 | Tower Sign, East (El. 44) | 5 | 0 | 02-Feb-15 A | 10-Feb-15 A | |

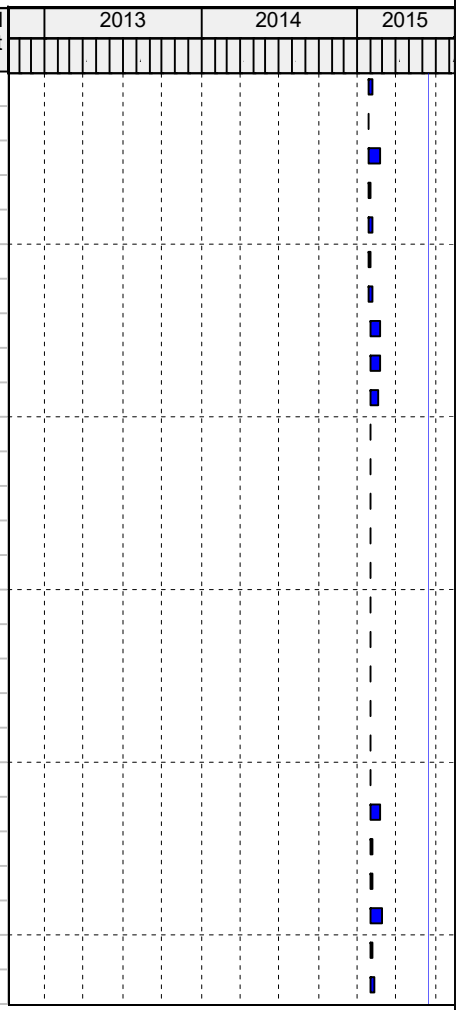



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8272 | GWB hang ceilings | 3 | 0 | 02-Feb-15 A | 04-Feb-15 A | |
| SW-2320 | Zone 3 - Pour ped pole base | 3 | 0 | 02-Feb-15 A | 05-Feb-15 A | |
| LL1-8156 | Install doors & hardware at corridors | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| L1B-6015 | HVAC drops at West Ballrooms | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L1B-6021 | Electrical drops at West Ballrooms | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L1B-6029 | HVAC drops at East Ballroom | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L1B-6031 | Electrical drops at East Ballroom | 5 | 0 | 02-Feb-15 A | 09-Feb-15 A | |
| L06-8226 | Install base at corridors | 1 | 0 | 02-Feb-15 A | 02-Feb-15 A | |
| GB410-104 | Complete vinyl wallcoverings - Levels 4-10 | 4 | 0 | 02-Feb-15 A | 17-Feb-15 A | |
| GB1117-102 | Complete painting - Levels 3, 11-16 | 3 | 0 | 02-Feb-15 A | 04-Feb-15 A | |
| SW-2234 | Zone 2 - FRP door curbs | 4 | 0 | 02-Feb-15 A | 05-Feb-15 A | |
| I-6950 | Resolve MEP/ceiling height conflicts | 1 | 0 | 02-Feb-15 A | 13-Mar-15 A | |
| L05-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L04-7138 | Electrical trim & finish | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L05-7138 | Electrical trim & finish | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L11-7134 | Flooring - VCT | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| SW-2022 | Zone 4 - Remove pedestrian protection on 110th Ave | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| L1L-8246 | Complete fire sprinkler RI @ ceilings | 2 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| LL1-8184 | Install storefront at Exercise Room | 1 | 0 | 03-Feb-15 A | 02-Mar-15 A | |
| L12-8422 | Floor prep | 1 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| L14-8422 | Floor prep | 1 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| L15-8422 | Floor prep | 1 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| I-5144 | Damper at BPF #8 - framing revisions | 1 | 0 | 03-Feb-15 A | 03-Feb-15 A | |
| I-5154 | Sprinkler pipe furring - GWB hang | 7 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| I-5166 | ASI 63 electrical revisions - insulation | 2 | 0 | 03-Feb-15 A | 04-Feb-15 A | |
| ASI62r1 | ASI No. 62 (Revised) - Civil Site Grading Revisions an | 0 | 0 | 03-Feb-15 A | | |
| L06-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 04-Feb-15 A | 04-Feb-15 A | |

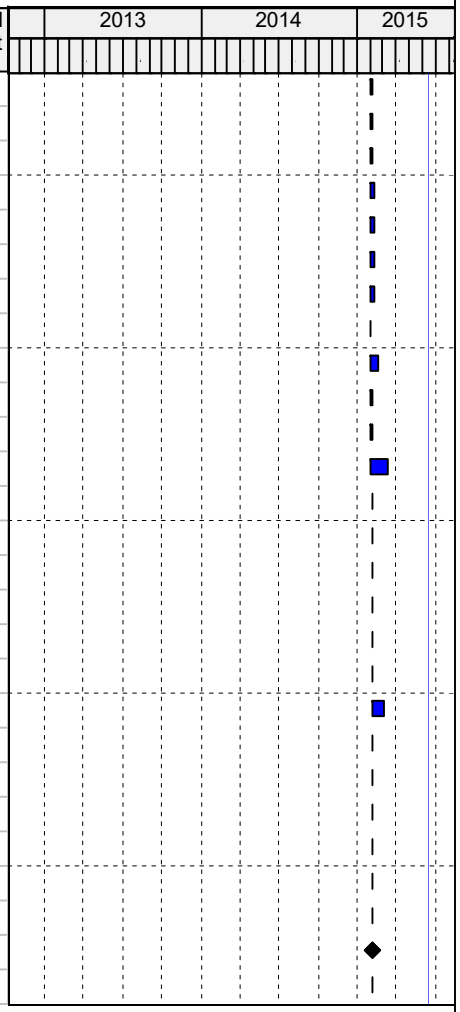



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-7134 | Flooring - VCT | 1 | 0 | 04-Feb-15 A | 04-Feb-15 A | |
| LL1-Z3-8142 | Ceramic tile in restrooms | 7 | 0 | 04-Feb-15 A | 20-Feb-15 A | |
| L1K-8144 | Paint, prime & first coat finish | 3 | 0 | 04-Feb-15 A | 09-Mar-15 A | |
| LL1-Z2-8158 | Wall coverings - vinyl at Meeting Rooms | 2 | 0 | 04-Feb-15 A | 05-Feb-15 A | |
| L09-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 06-Feb-15 A | |
| L10-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 09-Feb-15 A | |
| L11-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 09-Feb-15 A | |
| L16-8422 | Floor prep | 1 | 0 | 04-Feb-15 A | 10-Feb-15 A | |
| I-5146 | Damper at BPF #8 - complete GWB hang | 1 | 0 | 04-Feb-15 A | 04-Feb-15 A | |
| I-5168 | ASI 63 electrical revisions - vapor barrier | 2 | 0 | 04-Feb-15 A | 05-Feb-15 A | |
| L07-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 05-Feb-15 A | 05-Feb-15 A | |
| L14-7134 | Flooring - VCT | 1 | 0 | 05-Feb-15 A | 05-Feb-15 A | |
| L1L-8102a | GWB tape & finish walls & ceilings (Dining & Lounge) | 7 | 0 | 05-Feb-15 A | 12-Feb-15 A | |
| LL1-8170 | Flooring - tile at elevator lobby | 3 | 0 | 05-Feb-15 A | 09-Feb-15 A | |
| LL1-8186 | Wall coverings - vinyl at corridors | 5 | 0 | 05-Feb-15 A | 19-Feb-15 A | |
| L1B-6023 | Fire sprinkler drops at West Ballrooms | 5 | 0 | 05-Feb-15 A | 09-Feb-15 A | |
| L1B-6033 | Fire sprinkler drops at East Ballroom | 5 | 0 | 05-Feb-15 A | 09-Feb-15 A | |
| GB1117-106 | Complete flooring - Levels 3, 11-16 | 4 | 0 | 05-Feb-15 A | 10-Feb-15 A | |
| I-6100 | Resolve lighting/access panel conflict | 5 | 0 | 05-Feb-15 A | 13-Feb-15 A | |
| GB1117-104 | Complete vinyl wallcoverings - Levels 3, 11-16 | 5 | 0 | 05-Feb-15 A | 11-Feb-15 A | |
| L08-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 06-Feb-15 A | 06-Feb-15 A | |
| L15-7134 | Flooring - VCT | 1 | 0 | 06-Feb-15 A | 06-Feb-15 A | |
| MPP-1054 | Caulking - Elevation 3 (south elevation, west of manli | 3 | 0 | 06-Feb-15 A | 10-Feb-15 A | |
| ASI66 | ASI No. 66 - MDP Electrical Drawings Revision 23A | 0 | 0 | 06-Feb-15 A | | |
| L03-8418 | Flooring - carpet at Elevator Lobby | 2 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L04-8408 | Install base at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L05-8408 | Install base at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |

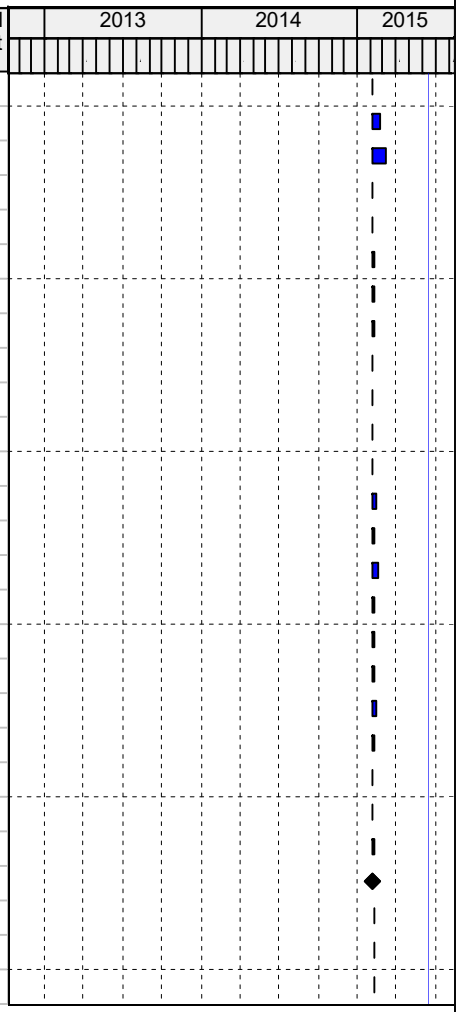



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8408 | Install base at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L09-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L16-7134 | Flooring - VCT | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L1K-8102a | GWB hang ceilings at Public Restroom | 2 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| LL2-2094 | Install doors & hardware at Laundry | 2 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| SW-2032 | Zone 4 - Demo existing trees & hardscapes | 3 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| CO-7139 | Install remaining devices & prep devices for testing - | 7 | 0 | 09-Feb-15 A | 03-Mar-15 A | |
| MPP-1024 | (B) Complete Elevation 4 (south elevation, east of tov | 2 | 0 | 09-Feb-15 A | 10-Feb-15 A | |
| L1L-8218 | Frame ceilings & inspection | 5 | 0 | 09-Feb-15 A | 12-Feb-15 A | |
| L1K-8136 | Ceiling grid & inspection | 4 | 0 | 09-Feb-15 A | 11-Feb-15 A | |
| L1L-8274 | GWB tape & finish walls & ceilings | 7 | 0 | 09-Feb-15 A | 24-Feb-15 A | |
| L15-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L16-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L17-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| L14-8131 | Bathrooms - Install access panels | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| I-5170 | ASI 63 electrical revisions - GWB hang, tape & finish | 7 | 0 | 09-Feb-15 A | 17-Feb-15 A | |
| SW-2058 | Zone 4 - Demo existing curb at 110th | 1 | 0 | 09-Feb-15 A | 09-Feb-15 A | |
| MPT-1114 | Cap metal - Porte Cochere | 3 | 0 | 09-Feb-15 A | 12-Feb-15 A | |
| I-5172 | Resolve Bar Area RFIs & complete revised work | 10 | 0 | 09-Feb-15 A | 04-Mar-15 A | |
| I-2960 | Lack of Stainless Steel Ceiling Closure Pieces (Shrou | 5 | 0 | 09-Feb-15 A | 13-Mar-15 A | |
| L07-8408 | Install base at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L08-8408 | Install base at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L09-8408 | Install base at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L10-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L11-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L17-7134 | Flooring - VCT | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L09-8224 | HVAC grilles & registers at corridors | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |

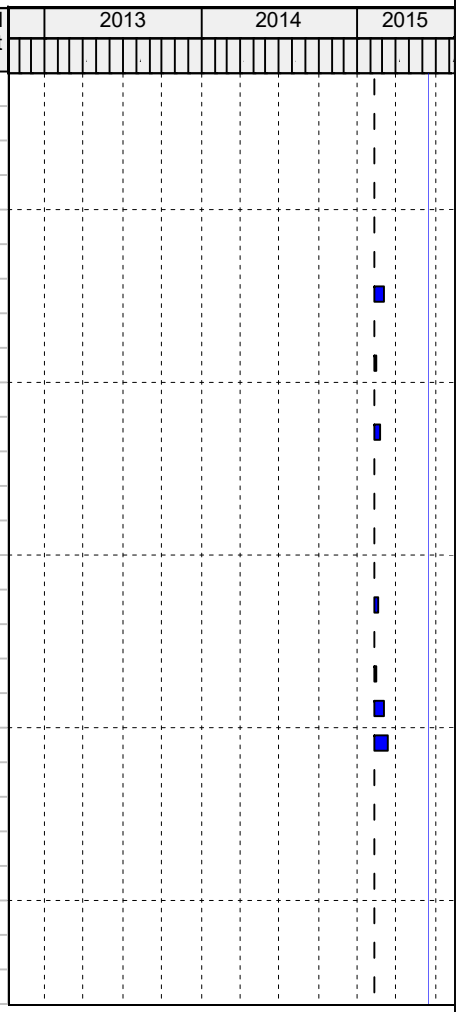



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8224 | HVAC grilles & registers at corridors | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| L07-8224 | HVAC grilles & registers at corridors | 1 | 0 | 10-Feb-15 A | 10-Feb-15 A | |
| SW-2036 | Zone 4 - Grade for curb and gutter | 2 | 0 | 10-Feb-15 A | 11-Feb-15 A | |
| CO-7140 | Fire Alarm System Device Testing - Tower Levels 4 thı | 7 | 0 | 10-Feb-15 A | 05-Mar-15 A | |
| L17-8422 | Floor prep | 1 | 0 | 10-Feb-15 A | 11-Feb-15 A | |
| MPT-1116 | Cap metal - Pool high roof | 3 | 0 | 10-Feb-15 A | 12-Feb-15 A | |
| ASI67 | ASI No. 67 - Meeting Room Door Hardware Revisions | 0 | 0 | 10-Feb-15 A | | |
| L10-8408 | Install base at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L11-8408 | Install base at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L12-8408 | Install base at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L12-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L14-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L03-7134 | Flooring - VCT | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| MPT-1018a | Install hi-roof cornice metal | 8 | 0 | 11-Feb-15 A | 08-Apr-15 A | |
| SW-2038 | Zone 4 - FRP curb & gutter | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| SW-2046 | Zone 4 - Install conduit | 2 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| L1K-8152 | Install doors & hardware | 3 | 0 | 11-Feb-15 A | 17-Feb-15 A | |
| L1L-8228 | GWB tape & finish | 7 | 0 | 11-Feb-15 A | 03-Mar-15 A | |
| SW-2054 | Zone 4 - Install flag pole bases | 3 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| L17-8226 | Install base at corridors | 1 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| MPP-1058 | (B) Install podium cornice, south/east | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| L03-8422 | Floor prep | 1 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| MPT-1108 | Cap metal - complete at tower | 5 | 0 | 11-Feb-15 A | 13-Feb-15 A | |
| MPT-1112 | Cap metal - complete at Ballroom roof | 3 | 0 | 11-Feb-15 A | 13-Feb-15 A | |
| CO-7404 | Cx - FPT - Heat Pumps | 3 | 0 | 11-Feb-15 A | 13-Feb-15 A | |
| L14-8408 | Install base at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L15-8408 | Install base at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |

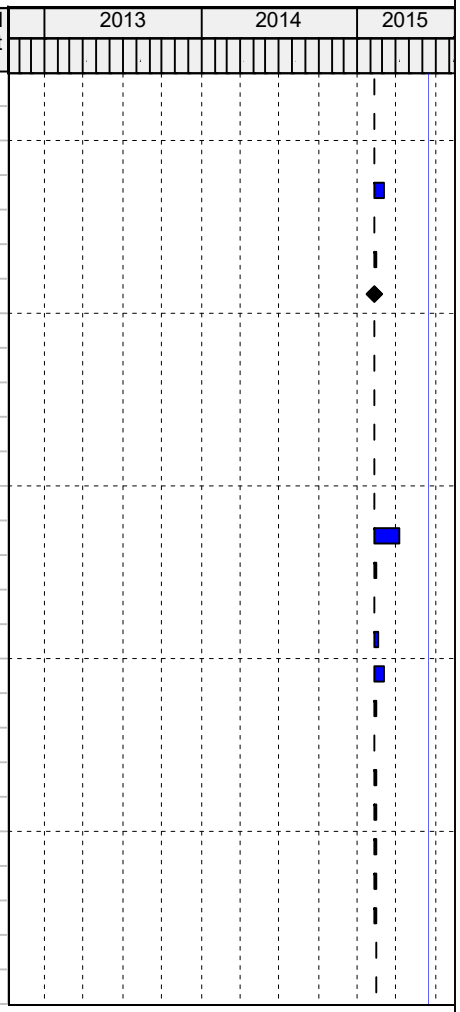



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L16-8408 | Install base at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L16-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L06-7138 | Electrical trim & finish | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| L1K-8102b | GWB tape & finish at Restrooms | 7 | 0 | 12-Feb-15 A | 25-Feb-15 A | |
| LL1-8154 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 12-Feb-15 A | 20-Feb-15 A | |
| ASI68 | ASI No. 68 - MDP Mechanical Drawings Revision 21 | 0 | 0 | 12-Feb-15 A | | |
| LL1-Z3-FCC28 | Electrical trim & finish at FCC | 4 | 0 | 12-Feb-15 A | 16-Feb-15 A | |
| LL1-8182 | Install doors & hardware at Exercise Room | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| GB1117-108 | Complete base - Levels 3, 11-16 | 5 | 0 | 12-Feb-15 A | 18-Feb-15 A | |
| GB1117-110 | Complete countertops - Levels 3, 11-16 | 1 | 0 | 12-Feb-15 A | 12-Feb-15 A | |
| GB1117-112 | Complete shower/tub surrounds - Levels 3, 11-16 | 3 | 0 | 12-Feb-15 A | 16-Feb-15 A | |
| L17-8408 | Install base at Elevator Lobby | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| L17-8418 | Flooring - carpet at Elevator Lobby | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| SW-2118 | Zone 1 - FRP sidewalk (NE corner) | 2 | 0 | 13-Feb-15 A | 13-Mar-15 A | |
| SW-2034 | Zone 4 - Install irrigation sleeves | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| SW-2060 | Zone 4 - Sawcut curb & gutter | 1 | 0 | 13-Feb-15 A | 13-Feb-15 A | |
| ASI69 | ASI No. 69 - Architectural Level 1 Revised Ceiling Plai | 0 | 0 | 13-Feb-15 A | | |
| LL1-Z2-8142 | Wall coverings - vinyl at corridors | 3 | 0 | 16-Feb-15 A | 19-Feb-15 A | |
| I-6900 | Resolve Garage EF motor/VFD issue (including corre | 20 | 0 | 16-Feb-15 A | 25-Mar-15 A | |
| I-5066 | RFI 848.1 -Flagpole Lighting - South Light/Flagpole E | 1 | 0 | 16-Feb-15 A | 16-Mar-15 A | |
| L03-7136 | Install doors & hardware | 2 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| MPP-1012 | Caulking - Elevation 4 (south elevation, east of tower) | 6 | 0 | 16-Feb-15 A | 23-Feb-15 A | |
| L10-8224 | HVAC grilles & registers at corridors | 1 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| L06-8224 | HVAC grilles & registers at corridors | 1 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| L05-8224 | HVAC grilles & registers at corridors | 1 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| SW-2040 | Zone 4 - Fine grade for sidewalk and planter curb | 3 | 0 | 16-Feb-15 A | 17-Feb-15 A | |

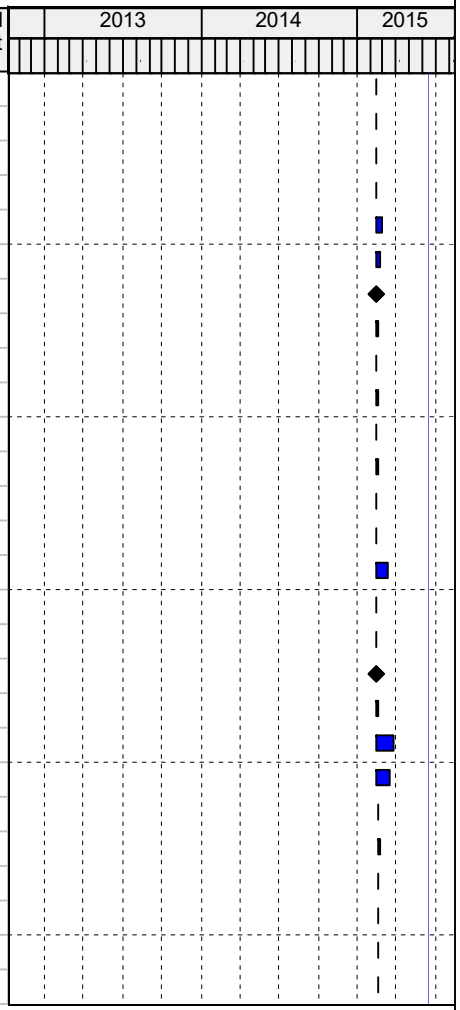



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| MPP-1036 | Podium Signs, East | 5 | 0 | 16-Feb-15 A | 18-Feb-15 A | |
| L1K-8150 | HVAC drops/trim at ceiling | 2 | 0 | 16-Feb-15 A | 17-Feb-15 A | |
| LL2-8146 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 16-Feb-15 A | 23-Feb-15 A | |
| LL1-8172 | Ceiling grid & inspection at Exercise Room (additional | 6 | 0 | 16-Feb-15 A | 23-Feb-15 A | |
| L1K-8162 | Complete wallcoverings (FRP) | 2 | 0 | 16-Feb-15 A | 17-Feb-15 A | |
| L1B-6011 | GWB, hang ceiling at West Ballrooms | 4 | 0 | 16-Feb-15 A | 18-Feb-15 A | |
| L1B-8138 | GWB hang, tape & finish ceilings at corridors (comple | 11 | 0 | 16-Feb-15 A | 03-Jun-15 A | |
| LL1-8176 | HVAC drops/trim to grid | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L03-8408 | Install base at Elevator Lobby | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L03-7034 | Install doors & hardware (x42) | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L03-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L07-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L08-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L09-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L10-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L11-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L12-7138 | Electrical trim & finish | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L16-7136 | Install doors & hardware | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| LL2-2062 | Ceiling grid at Laundry | 4 | 0 | 17-Feb-15 A | 30-Mar-15 A | |
| L15-8224 | HVAC grilles & registers at corridors | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L14-8224 | HVAC grilles & registers at corridors | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| CO-7258 | Cx - Start-Up - KMUA Trane (2) | 2 | 0 | 17-Feb-15 A | 20-Feb-15 A | |
| SW-2044 | Zone 4 - FRP sidewalk (SW corner remaining) | 3 | 0 | 17-Feb-15 A | 02-Apr-15 A | |
| LL1-Z3-FCC30 | Data/phone trim/finish at FCC | 4 | 0 | 17-Feb-15 A | 19-Feb-15 A | |
| LL1-Z3-6036 | GWB hang, tape & finish ceiling at Food Prep (Dry St | 5 | 0 | 17-Feb-15 A | 02-Mar-15 A | |
| MPT-1092 | Caulking - Elevation 31 (above L12 terrace, west elev | 4 | 0 | 17-Feb-15 A | 20-Feb-15 A | |
| MPT-1098 | Caulking - Elevation 30 (south elevation, west of man | 6 | 0 | 17-Feb-15 A | 23-Mar-15 A | |

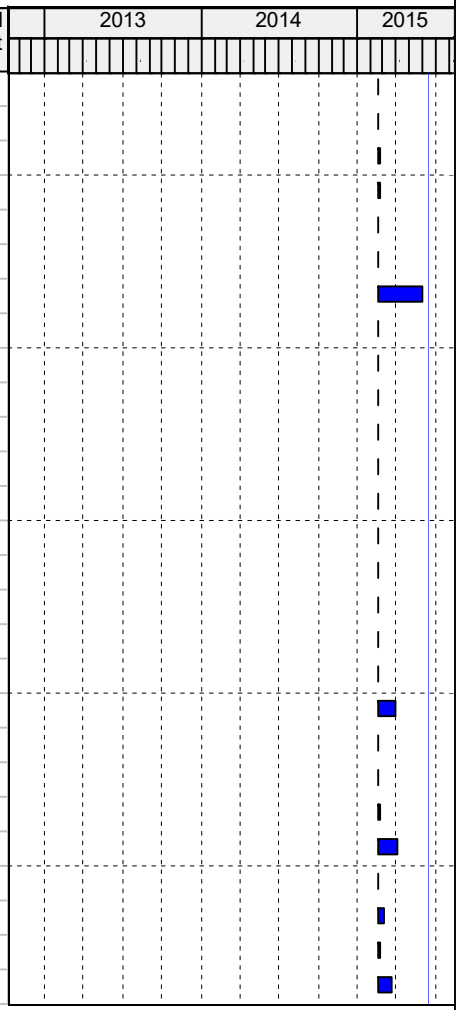



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-6014Id2 | L1 bar redesign - install wall coverings at MR9 | 1 | 0 | 17-Feb-15 A | 17-Feb-15 A | |
| L1K-8146 | Fire sprinkler drops/trim at ceiling | 1 | 0 | 17-Feb-15 A | 10-Mar-15 A | |
| L1K-8148 | Lighting & electrical trim at ceiling | 2 | 0 | 17-Feb-15 A | 10-Mar-15 A | |
| GB1117-114 | Complete plumbing fixture installation - Levels 3, 11-1 | 4 | 0 | 17-Feb-15 A | 20-Feb-15 A | |
| L1K-8164 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 17-Feb-15 A | 10-Mar-15 A | |
| MPT-1062 | Elevation 32 metal panels (south elevation, east of m | 8 | 0 | 18-Feb-15 A | 26-Mar-15 A | |
| L14-7138 | Electrical trim & finish | 1 | 0 | 18-Feb-15 A | 18-Feb-15 A | |
| L15-7138 | Electrical trim & finish | 1 | 0 | 18-Feb-15 A | 18-Feb-15 A | |
| L17-7138 | Electrical trim & finish | 1 | 0 | 18-Feb-15 A | 18-Feb-15 A | |
| CO-7262 | Cx - Start-Up - Electric Unit Heaters | 3 | 0 | 18-Feb-15 A | 30-Mar-15 A | |
| LL1-8174 | Wall coverings - vinyl at Exercise Room | 2 | 0 | 18-Feb-15 A | 19-Feb-15 A | |
| L1B-6017 | GWB, hang ceiling at East Ballrooms | 4 | 0 | 18-Feb-15 A | 20-Feb-15 A | |
| SW-2062 | Zone 4 - Patch curb & gutter | 2 | 0 | 18-Feb-15 A | 19-Feb-15 A | |
| CO-7256 | Cx - Start-Up - Elevator Machine Room Ductless Split | 1 | 0 | 19-Feb-15 A | 19-Feb-15 A | |
| LL1-8178 | Lighting & electrical drops to grid | 2 | 0 | 19-Feb-15 A | 20-Feb-15 A | |
| LL1-8180 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 19-Feb-15 A | 20-Feb-15 A | |
| GB410-110 | Complete countertops - Levels 4-10 | 1 | 0 | 19-Feb-15 A | 19-Feb-15 A | |
| GB410-112 | Complete shower/tub surrounds - Levels 4-10 | 1 | 0 | 19-Feb-15 A | 19-Feb-15 A | |
| GB410-118 | Complete barn doors - Levels 4-10 | 1 | 0 | 19-Feb-15 A | 19-Feb-15 A | |
| GB1117-118 | Complete barn doors - Levels 3, 11-16 | 2 | 0 | 19-Feb-15 A | 20-Feb-15 A | |
| LL1-Z2-8160a | Flooring - carpet at Meeting Rooms | 2 | 0 | 19-Feb-15 A | 23-Feb-15 A | |
| LL2-2098 | HVAC drops to grid at Laundry | 2 | 0 | 20-Feb-15 A | 04-Mar-15 A | |
| LL2-2088 | Lighting & electrical drops to grid at Laundry | 2 | 0 | 20-Feb-15 A | 09-Mar-15 A | |
| L1K-8123 | Floor prep | 2 | 0 | 20-Feb-15 A | 23-Feb-15 A | |
| LL1-8158 | Floor prep at corridors | 2 | 0 | 20-Feb-15 A | 23-Feb-15 A | |
| L1B-8102a | GWB, tape & finish ceiling at West Ballroom | 7 | 0 | 20-Feb-15 A | 02-Mar-15 A | |
| GB410-114 | Complete plumbing fixture installation - Levels 4-10 | 3 | 0 | 20-Feb-15 A | 24-Feb-15 A | |

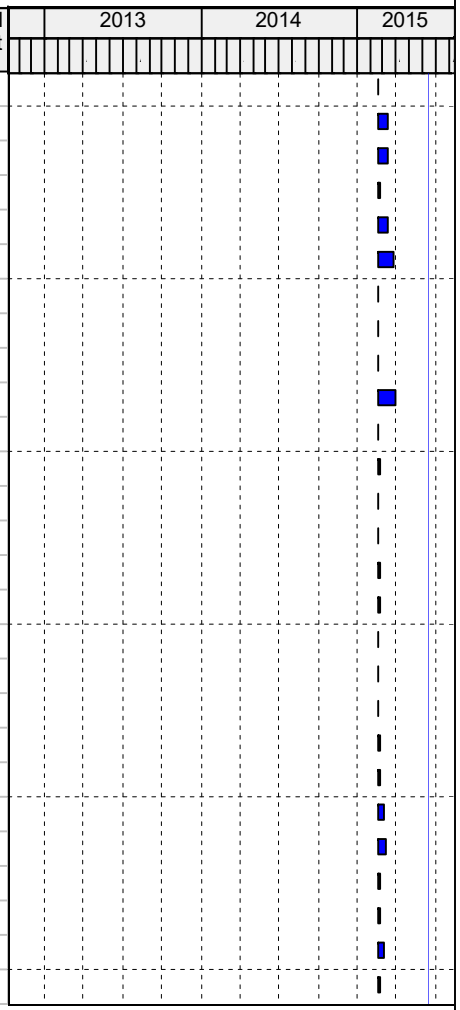



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2106 | Floor prep | 1 | 0 | 20-Feb-15 A | 20-Feb-15 A | |
| LL2-2086 | Flooring - epoxy remainder of floor (including prep) | 6 | 0 | 21-Feb-15 A | 26-Feb-15 A | |
| MPT-1102 | Elevation 32 spandrel panels (south elevation, east o | 2 | 0 | 21-Feb-15 A | 16-Mar-15 A | |
| LL2-2104 | Flooring - epoxy at equipment alcoves | 5 | 0 | 21-Feb-15 A | 26-Feb-15 A | |
| LL1-Z3-8164 | Field measure & fabricate countertops | 15 | 0 | 21-Feb-15 A | 23-Apr-15 A | |
| LL1-8116f | Fabricate & deliver countertops | 10 | 0 | 21-Feb-15 A | 23-Apr-15 A | |
| LL1-Z2-8118a | Install decorative light fixtures | 3 | 0 | 23-Feb-15 A | 03-Mar-15 A | |
| LL1-Z2-8124a | Install base | 10 | 0 | 23-Feb-15 A | 27-Feb-15 A | |
| CO-7400 | Cx - 3rd Party Cx of Mechanical, Plumbing, Electrical | 40 | 0 | 23-Feb-15 A | 05-Jun-15 A | |
| LL1-Z3-8144 | Install toilets at Restrooms | 4 | 0 | 23-Feb-15 A | 27-Feb-15 A | |
| LL1-8166 | Install base at corridors | 5 | 0 | 23-Feb-15 A | 27-Feb-15 A | |
| LL1-Z2-8122 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 23-Feb-15 A | 09-Mar-15 A | |
| GB1117-116 | Complete shower doors - Levels 3, 11-16 | 2 | 0 | 23-Feb-15 A | 24-Feb-15 A | |
| L17-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| L16-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| L12-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| L11-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| L03-8224 | HVAC grilles & registers at corridors | 1 | 0 | 24-Feb-15 A | 24-Feb-15 A | |
| MPT-1100 | Install spandrel, east (Elevation 44) | 2 | 0 | 24-Feb-15 A | 26-Feb-15 A | |
| SW-2064 | Porte Cochere - Fill and grade Porte Cochere drive | 3 | 0 | 24-Feb-15 A | 06-Mar-15 A | |
| L1BOH2-8104 | Paint, prime | 2 | 0 | 24-Feb-15 A | 13-Apr-15 A | |
| L1K-8124a | Flooring - epoxy - east end | 5 | 0 | 24-Feb-15 A | 26-Feb-15 A | |
| LL2-8148 | Fire sprinkler drops to grid | 1 | 0 | 24-Feb-15 A | 09-Mar-15 A | |
| LL1-8162 | Flooring - carpet at corridors | 5 | 0 | 24-Feb-15 A | 02-Mar-15 A | |
| LL1-Z2-8128 | HVAC trim at ceiling | 1 | 0 | 24-Feb-15 A | 03-Mar-15 A | |
| LL1-Z2-8130 | Fire sprinkler trim | 1 | 0 | 24-Feb-15 A | 04-Mar-15 A | |
| MPT-1052 | Elevation 48/49 (north elevation, east of 51, L3-L17) | 3 | 0 | 25-Feb-15 A | 11-Mar-15 A | |

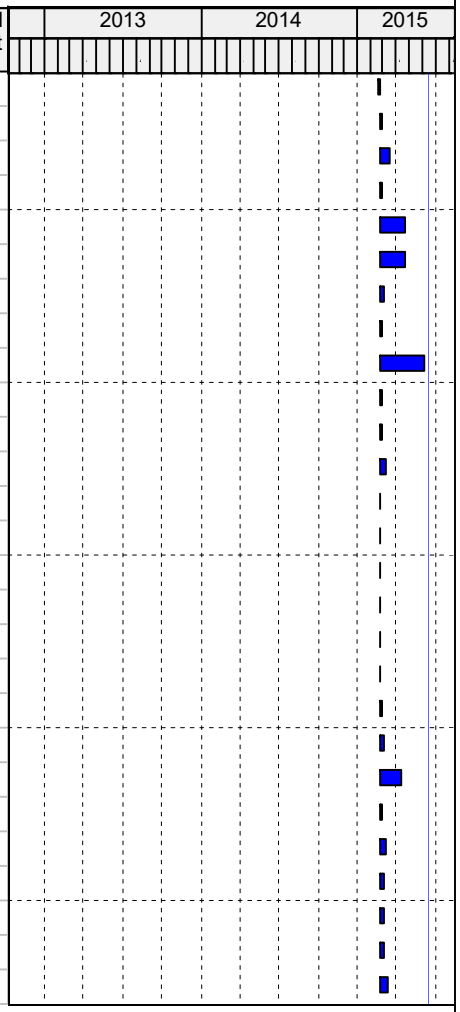



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7100T | Cx - Start-Up - Life Safety Exhaust Fans and VFD's | 13 | 0 | 25-Feb-15 A | 03-Apr-15 A | |
| EL-6044 | Elev 6 - Electrical trim & finish | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| EL-6046 | Elev 6 - Fire alarm trim | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| EL-6048 | Elev 6 - Fire sprinkler trim | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| EL-6050 | Elev 6 - Install pit grates | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| L1L-8276 | Paint, prime & first coat finish | 3 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| GB410-116 | Complete shower doors - Levels 4-10 | 2 | 0 | 25-Feb-15 A | 26-Feb-15 A | |
| L1BOH2-8114 | Ceiling grid & inspection | 4 | 0 | 26-Feb-15 A | 18-Mar-15 A | |
| SW-2066 | Porte Cochere - FRP planter curb | 2 | 0 | 26-Feb-15 A | 27-Feb-15 A | |
| L03-8684 | Pourback piping trench | 1 | 0 | 26-Feb-15 A | 26-Feb-15 A | |
| AS70 | ASI No. 70 - Site Illumination Plan | 0 | 0 | 26-Feb-15 A | | |
| I-5082 | ASI 70 - Site Illumination Plan | 0 | 0 | 26-Feb-15 A | | |
| L1BOH2-8200 | Paint, first coat finish | 1 | 0 | 26-Feb-15 A | 13-Apr-15 A | |
| CO-7220 | Cx - Start-Up - Common Space Heat Pump | 4 | 0 | 26-Feb-15 A | 12-May-15 A | |
| I-3102 | GWB, tape & finish ceiling at East Ballroom | 7 | 0 | 26-Feb-15 A | 06-Mar-15 A | |
| I-5124 | Dining feature wall - install plywood backing | 1 | 0 | 26-Feb-15 A | 26-Feb-15 A | |
| L03-8686 | Cure piping trench | 14 | 0 | 27-Feb-15 A | 12-Mar-15 A | |
| L1L-8114a | Install 9-wood celing supports - south of Grid K | 3 | 0 | 27-Feb-15 A | 04-Mar-15 A | |
| L1K-8124b | Flooring - epoxy - west end (including prep) | 7 | 0 | 27-Feb-15 A | 06-Mar-15 A | |
| CO-7104T | Fire Alarm & Smoke Control Pre-Testing (Tower) - Tow | 3 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7112T | City of Bellevue/3rd Party Fire Sprinkler Inspection / A | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7118T | City of Bellevue/3rd Party Fire Alarm Inspection / Appl | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7106T | City of Bellevue/3rd Party Smoke Control Testing (Tow | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7412 | Cx - Pressure Testing - GC Indicates Podium Complet | 0 | 0 | | 01-Mar-15 A | |
| CO-7416 | Cx - Pressure Testing - Pre-Walk with GC (Podium) [Dl | 1 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7418 | Cx - Pressure Testing - GC Makes Corrections (Podiu | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7420 | Cx - Pressure Testing - Pressure Pre-Test (Podium) [D | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |

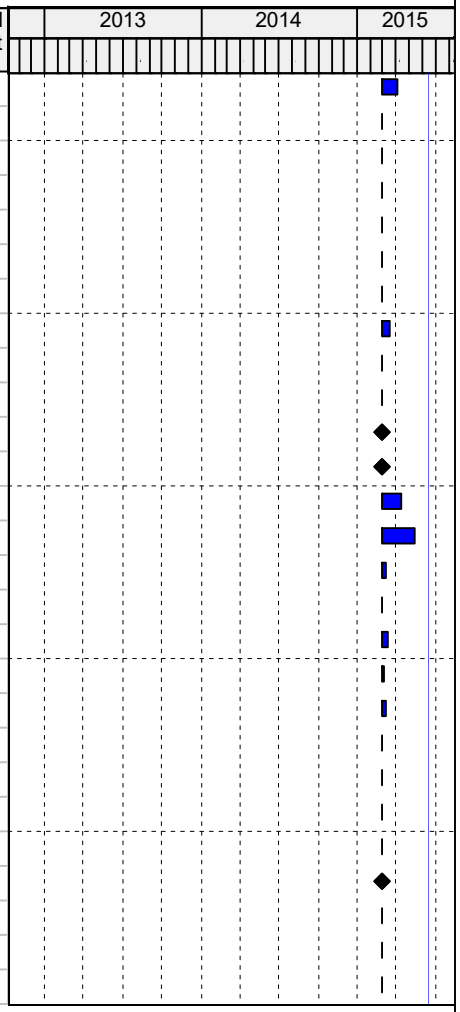


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7422 | Cx - Pressure Testing -Corrections (Podium) [DELETE | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7424 | Cx - Pressure Testing - Pressure Final Test [DELETED | 1 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7426 | Cx - Pressure Testing - Building Final Corrections [DEI | 1 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7142 | Fire Alarm System Device Testing - Podium [DELETEI | 7 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7428 | Cx - Pressure Testing - GC Indicates Tower Complete | 0 | 0 | | 01-Mar-15 A | |
| CO-7430 | Cx - Pressure Testing - Pre-Walk with GC (Tower) [DEI | 1 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7432 | Cx - Pressure Testing - GC Makes Corrections (Tower) | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7434 | Cx - Pressure Testing - Pressure Pre-Test (Tower) [DEI | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7436 | Cx - Pressure Testing -Corrections (Tower) [DELETED, | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| SW-2042 | Porte Cochere - Install trench drain | 3 | 0 | 02-Mar-15 A | 04-Mar-15 A | |
| SW-2128 | Zone 1 - FRP planter wall at NE corner | 8 | 0 | 02-Mar-15 A | 04-Mar-15 A | |
| SW-2130 | Zone 1 - Waterproof wall | 2 | 0 | 02-Mar-15 A | 02-Mar-15 A | |
| LL1-Z3-FCC36 | Install doors & hardware at FCC | 2 | 0 | 02-Mar-15 A | 02-Mar-15 A | |
| LL1-8136 | Ceramic tile in restrooms | 3 | 0 | 02-Mar-15 A | 04-Mar-15 A | |
| L1K-8218 | Floor prep | 2 | 0 | 02-Mar-15 A | 02-Mar-15 A | |
| L17-9012 | Complete Shower Surrounds | 2 | 0 | 02-Mar-15 A | 24-Apr-15 A | |
| LL2-2048 | Set Laundry Room equipment (BY OTHERS) | 1 | 0 | 03-Mar-15 A | 06-Mar-15 A | |
| L1K-8210 | Ceramic tile in restrooms | 7 | 0 | 03-Mar-15 A | 17-Mar-15 A | |
| MPT-1060 | Elevation 33/34 hat channel (east elevation, south er | 3 | 0 | 03-Mar-15 A | 10-Mar-15 A | |
| LL1-8142 | Plumbing fixtures & trim | 2 | 0 | 03-Mar-15 A | 04-Mar-15 A | |
| LL1-Z3-6038 | Paint ceiling at Food Prep (Dry Storage) | 2 | 0 | 03-Mar-15 A | 04-Mar-15 A | |
| L1B-6019 | Frame ceiling clouds | 7 | 0 | 03-Mar-15 A | 06-Mar-15 A | |
| LL1-Z3-8160 | Install doors & hardware at restrooms | 2 | 0 | 03-Mar-15 A | 04-Mar-15 A | |
| L17-9004 | Complete Flooring & Base | 3 | 0 | 03-Mar-15 A | 15-Apr-15 A | |
| CO-7116T | Fire Alarm Pre-Testing (Tower) - Tower Levels 4 thru 1( | 6 | 0 | 04-Mar-15 A | 05-Mar-15 A | |
| LL1-8150 | Install bathroom accessories | 2 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L1L-8142 | HVAC drops to 9-wood ceiling - north of Grid K | 2 | 0 | 04-Mar-15 A | 18-Mar-15 A | |

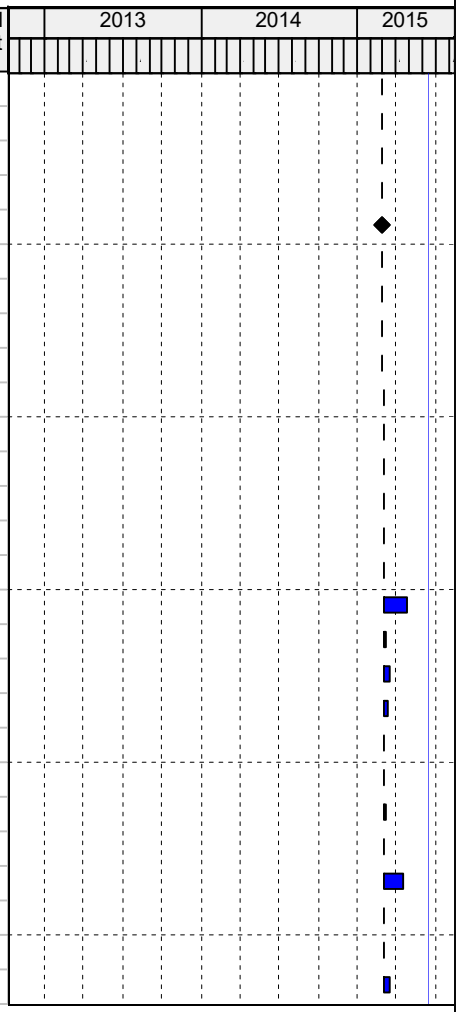


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8144 | Electrical drops to 9-wood ceiling - north of Grid K | 2 | 0 | 04-Mar-15 A | 18-Mar-15 A | |
| L1L-8146 | Fire sprinkler drops to 9-wood ceiling - north of Grid K | 2 | 0 | 04-Mar-15 A | 18-Mar-15 A | |
| CO-7110T | Fire Sprinkler Pre-Testing (Tower) - Tower Levels 4 thru | 6 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| CO-7110T.1 | Fire Sprinkler Pre-Testing (Tower) - Tower Levels 3, 11 | 2 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| LL1-Z2-8150 | Install base at corridors | 3 | 0 | 05-Mar-15 A | 06-Mar-15 A | |
| L1L-8108 | GWB hang walls & ceilings (Bar) | 2 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L17-9000 | Complete GWB (1714 & 1718) | 5 | 0 | 06-Mar-15 A | 11-Mar-15 A | |
| LL1-Z2-8123 | Floor prep | 1 | 0 | 06-Mar-15 A | 06-Mar-15 A | |
| L1L-8110 | GWB tape & finish walls & ceilings (Bar) | 7 | 0 | 06-Mar-15 A | 12-Mar-15 A | |
| EL-1238 | Elev 1&2 - 30-day correction period | 30 | 0 | 07-Mar-15 A | 10-Apr-15 A | |
| L03-8624 | Fire sprinkler trim at Pool | 2 | 0 | 09-Mar-15 A | 09-Mar-15 A | |
| L11-7032 | Flooring - VCT (x42) | 1 | 0 | 09-Mar-15 A | 09-Mar-15 A | |
| SW-2212 | Zone 2 - FRP sidewalk panels | 3 | 0 | 09-Mar-15 A | 12-Mar-15 A | |
| SW-2048 | Porte Cochere - FRP Porte Cochere drive | 10 | 0 | 09-Mar-15 A | 31-Mar-15 A | |
| L03-8666 | Electrical trim & finish at ceiling at Pool | 2 | 0 | 09-Mar-15 A | 11-Mar-15 A | |
| CO-7139.1 | Install remaining devices & prep devices for testing - T | 6 | 0 | 09-Mar-15 A | 12-Mar-15 A | |
| SW-2222 | Zone 2 - Install j-box at NE corner | 1 | 0 | 09-Mar-15 A | 09-Mar-15 A | |
| LL1-Z2-8146 | Floor prep at corridors | 2 | 0 | 09-Mar-15 A | 10-Mar-15 A | |
| L1L-8292 | GWB hang ceilings | 2 | 0 | 09-Mar-15 A | 10-Mar-15 A | |
| CO-7140.1 | Fire Alarm System Device Testing - Tower Levels 4 thr | 6 | 0 | 09-Mar-15 A | 12-Mar-15 A | |
| L1B-6025 | MEP drops at celing clouds (including inspection) | 7 | 0 | 09-Mar-15 A | 18-Mar-15 A | |
| L1L-8230 | Paint, prime & first coat finish | 3 | 0 | 10-Mar-15 A | 10-Mar-15 A | |
| LL2-2100 | Fire sprinkler drops to grid at Laundry | 1 | 0 | 10-Mar-15 A | 10-Mar-15 A | |
| LL1-Z2-8148 | Flooring - carpet at corridors | 3 | 0 | 10-Mar-15 A | 12-Mar-15 A | |
| L1B-8206 | Ceiling grid at West Ballrooms | 3 | 0 | 10-Mar-15 A | 11-Mar-15 A | |
| CM-1024 | Tower - "Clean/Punch" Complete - All Floors [DELETE | 0 | 0 | | 10-Mar-15 A | |
| MPT-1064 | Elevation 33/34 metal panels (east elevation, south e | 7 | 0 | 11-Mar-15 A | 26-Mar-15 A | |

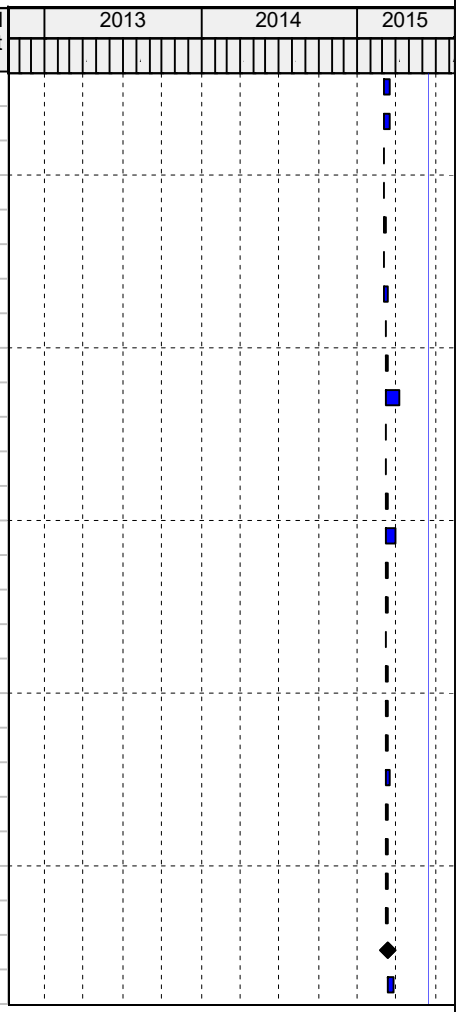



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z2-8160 | Flooring - carpet at Jr. Ballroom | 3 | 0 | 11-Mar-15 A | 13-Mar-15 A | |
| L1L-8258 | GWB tape & finish walls & ceilings | 7 | 0 | 11-Mar-15 A | 17-Mar-15 A | |
| L1BOH2-8120 | Wall coverings - vinyl | 3 | 0 | 12-Mar-15 A | 04-May-15 A | |
| L1B-8208 | Ceiling grid at East Ballroom | 3 | 0 | 12-Mar-15 A | 13-Mar-15 A | |
| L17-9002 | Complete Painting | 2 | 0 | 12-Mar-15 A | 13-Mar-15 A | |
| L1L-8154 | Paint, prime & first finish coat (Bar) | 2 | 0 | 13-Mar-15 A | 13-Mar-15 A | |
| L1K-8206 | Install toilets at restrooms | 2 | 0 | 16-Mar-15 A | 17-Mar-15 A | |
| MPT-1082 | Caulking - Elevation 48/49 (north elevation, east of 5 | 4 | 0 | 16-Mar-15 A | 19-Mar-15 A | |
| CO-7116T.1 | Smoke Control Equipment Pre-Testing (Fans & Damp | 5 | 0 | 16-Mar-15 A | 20-Mar-15 A | |
| LL1-8128 | Floor prep at Exercise Room | 2 | 0 | 16-Mar-15 A | 16-Mar-15 A | |
| LL1-Z2-8136 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 16-Mar-15 A | 30-Mar-15 A | |
| LL4-8136 | Clear out and clean parking area | 10 | 0 | 16-Mar-15 A | 04-Jun-15 A | |
| LL3-8136 | Clear out and clean parking area | 10 | 0 | 16-Mar-15 A | 05-Jun-15 A | |
| L1L-8142a | HVAC drops to 9-wood ceiling - south of Grid K | 2 | 0 | 16-Mar-15 A | 16-Mar-15 A | |
| L1L-8144a | Electrical drops to 9-wood ceiling - south of Grid K | 2 | 0 | 16-Mar-15 A | 16-Mar-15 A | |
| L1L-8146a | Fire sprinkler drops to 9-wood ceiling - south of Grid K | 2 | 0 | 16-Mar-15 A | 16-Mar-15 A | |
| L1K-8114a | Celing grid & inspection (west end) | 2 | 0 | 16-Mar-15 A | 19-Mar-15 A | |
| CM-1016c | CM - Owner FF+E "Build-Out" - Floors 6 & 7 | 7 | 0 | 16-Mar-15 A | 22-Mar-15 A | |
| LL2-2118 | Fabricate and deliver washing machine pedestal | 10 | 0 | 16-Mar-15 A | 18-Mar-15 A | |
| I-6902 | RFI 944 - Master control panel | 5 | 0 | 16-Mar-15 A | 03-Apr-15 A | |
| LL1-8138 | Flooring - install cork floor at Exercise Room | 3 | 0 | 17-Mar-15 A | 19-Mar-15 A | |
| LL1-Z3-8206 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 17-Mar-15 A | 23-Mar-15 A | |
| L1L-8302 | Lighting & electrical trim at ceilings | 3 | 0 | 17-Mar-15 A | 18-Mar-15 A | |
| L1K-8120 | Lighting & electrical trim at ceiling | 2 | 0 | 18-Mar-15 A | 19-Mar-15 A | |
| MPP-1020 | Elevation 18/19/21/22 & complete 45 (north elevatior | 12 | 0 | 18-Mar-15 A | 27-Mar-15 A | |
| I-1208 | Paint, prime & first coat finish | 2 | 0 | 18-Mar-15 A | 19-Mar-15 A | |
| L1L-8306 | Fire sprinkler trim | 1 | 0 | 18-Mar-15 A | 18-Mar-15 A | |

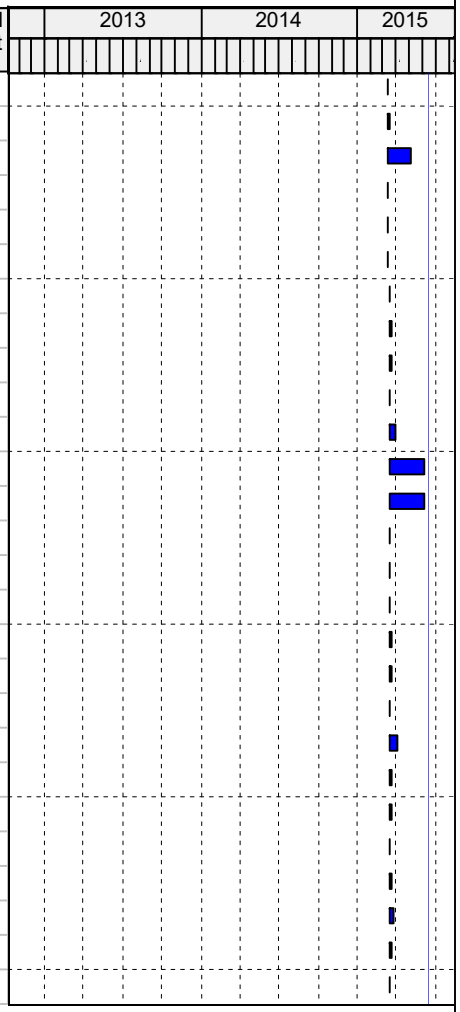



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8128 | Install die wall (Bar) | 3 | 0 | 19-Mar-15 A | 23-Mar-15 A | |
| L1B-6037 | GWB ceiling clouds | 5 | 0 | 19-Mar-15 A | 01-Apr-15 A | |
| LL2-2114 | Install washing machine pedestal | 2 | 0 | 19-Mar-15 A | 20-Mar-15 A | |
| I-5202 | Wall and soffit modifications | 4 | 0 | 19-Mar-15 A | 03-Apr-15 A | |
| LL1-Z3-FCC34 | Paint, final coat & touch-up up at FCC | 2 | 0 | 20-Mar-15 A | 20-Mar-15 A | |
| LL2-2112 | Set washing machines | 1 | 0 | 20-Mar-15 A | 20-Mar-15 A | |
| LL1-Z3-FCC32 | Flooring - VCT at FCC | 2 | 0 | 21-Mar-15 A | 21-Mar-15 A | |
| L1BOH2-8126 | Install doors & hardware | 3 | 0 | 23-Mar-15 A | 31-Mar-15 A | |
| L1K-8128 | Install Kitchen equipment (BY OTHERS) | 5 | 0 | 23-Mar-15 A | 21-Apr-15 A | |
| L04-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L05-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L06-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L07-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L08-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L09-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L10-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 23-Mar-15 A | 23-Mar-15 A | |
| L02-8130 | Ceiling grid at south half | 3 | 0 | 23-Mar-15 A | 26-Mar-15 A | |
| CO-7226 | Cx - Start-Up - Misc. Equipment | 5 | 0 | 23-Mar-15 A | 27-Mar-15 A | |
| L1BOH2C-6024 | Lighting & electrical trim at ceiling | 2 | 0 | 23-Mar-15 A | 14-Apr-15 A | |
| L1L-8136 | Install Peter Glassford art wall | 5 | 0 | 23-Mar-15 A | 27-Mar-15 A | |
| L1L-8282 | Finish carpentry/millwork | 5 | 0 | 23-Mar-15 A | 10-Apr-15 A | |
| LL1-8186a | Wall coverings - complete vinyl at corridors | 2 | 0 | 23-Mar-15 A | 24-Mar-15 A | |
| CM-1016d | CM - Owner FF+E "Build-Out" - Floors 8 & 9 | 7 | 0 | 23-Mar-15 A | 29-Mar-15 A | |
| L02-8184 | Build Kitchen exhaust shaft | 5 | 0 | 23-Mar-15 A | 27-Mar-15 A | |
| L1L-8294 | Ceiling coverings - vinyl | 3 | 0 | 23-Mar-15 A | 25-Mar-15 A | |
| L11-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L12-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |

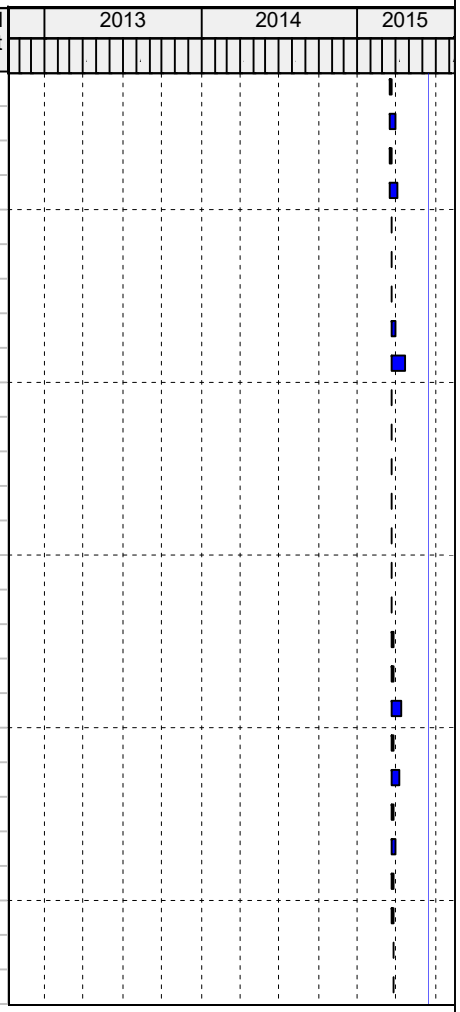


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L15-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L16-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L17-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L1K-8122 | Fire sprinkler drops/trim at ceiling | 1 | 0 | 24-Mar-15 A | 24-Mar-15 A | |
| L1K-8130 | HVAC drops/trim at celing | 2 | 0 | 24-Mar-15 A | 25-Mar-15 A | |
| L1K-8160 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 24-Mar-15 A | 25-Mar-15 A | |
| L17-9016 | Complete Shower Doors | 2 | 0 | 24-Mar-15 A | 06-May-15 A | |
| I-7010 | RFI 946 - Alterations to bar for epoxy flooring cove | 3 | 0 | 24-Mar-15 A | 30-Mar-15 A | |
| L1L-8310 | Install 9-wood ceiling supports at Sitting Area | 2 | 0 | 25-Mar-15 A | 26-Mar-15 A | |
| L1BOH2-8204 | HVAC drops/trim at ceiling | 2 | 0 | 25-Mar-15 A | 26-Mar-15 A | |
| MPT-1038 | Install louvers, north | 3 | 0 | 25-Mar-15 A | 20-Apr-15 A | |
| MPP-1048 | Caulking - Porte Cochere cornice metal | 3 | 0 | 25-Mar-15 A | 27-Mar-15 A | |
| L02-8148 | Paint at Locker Rooms | 2 | 0 | 25-Mar-15 A | 06-Apr-15 A | |
| L1K-8124a2 | Install doors & hardware | 2 | 0 | 25-Mar-15 A | 02-Apr-15 A | |
| L1L-8260 | Wall coverings - vinyl | 2 | 0 | 25-Mar-15 A | 26-Mar-15 A | |
| MPT-1106 | Install alcoves | 3 | 5 | 25-Mar-15 A | 19-Jun-15 | 2 |
| MPT-1110 | Cap metal at hi-roof | 3 | 0 | 25-Mar-15 A | 29-May-15 A | |
| L1L-8152 | Install ceiling (Bar) | 3 | 0 | 25-Mar-15 A | 15-Apr-15 A | |
| L1L-8116a | Finish carpentry/millwork - south of Grid K | 5 | 0 | 25-Mar-15 A | 21-Apr-15 A | |
| LL1-Z2-8142a | Wall coverings - complete vinyl at corridors | 1 | 0 | 25-Mar-15 A | 25-Mar-15 A | |
| L17-9008 | Complete Fire Sprinkler Trim | 1 | 0 | 25-Mar-15 A | 25-Mar-15 A | |
| CO-7222 | Cx - Start-Up - Kitchen Exhaust Fans | 2 | 0 | 26-Mar-15 A | 26-Mar-15 A | |
| L1K-8128a | Kitchen Equipment Final Connections | 10 | 0 | 26-Mar-15 A | 15-May-15 A | |
| CO-7260 | Cx - Start-Up - Ballroom AAON RTU | 1 | 0 | 26-Mar-15 A | 26-Mar-15 A | |
| L1L-8148 | Electrical rough-in at die wall (Bar) | 4 | 0 | 26-Mar-15 A | 31-Mar-15 A | |
| L17-9006 | Complete Lighting & Electrical Trim | 2 | 0 | 26-Mar-15 A | 31-Mar-15 A | |

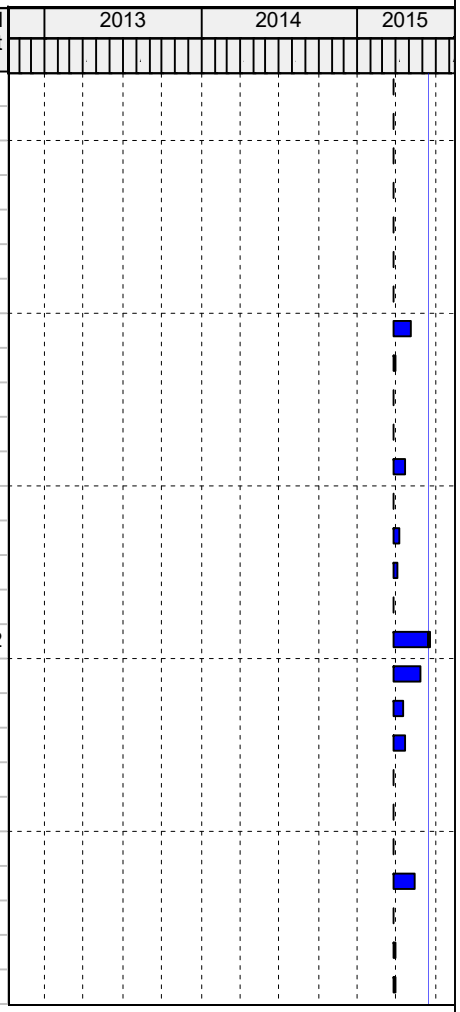



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-5084 | Zone 3 - FRP door apron at SE corner | 2 | 0 | 26-Mar-15 A | 27-Mar-15 A | |
| LL2-2116 | Relocate dryers and remove floor coping at dryer area | 3 | 0 | 26-Mar-15 A | 27-Mar-15 A | |
| L1B-8176 | Complete shaft wall at Prefunction 1 south end | 4 | 0 | 26-Mar-15 A | 02-Apr-15 A | |
| L1L-8206 | Lighting & electrical trim at ceilings - north of Grid K | 2 | 0 | 26-Mar-15 A | 31-Mar-15 A | |
| LL1-Z3-8128 | Flooring - VCT | 5 | 0 | 27-Mar-15 A | 10-Apr-15 A | |
| L1L-8312 | HVAC drops to 9-wood ceiling | 2 | 0 | 27-Mar-15 A | 02-Apr-15 A | |
| L1L-8314 | Electrical drops to 9-wood ceiling | 2 | 0 | 27-Mar-15 A | 02-Apr-15 A | |
| L1L-8316 | Fire sprinkler drops to 9-wood ceiling | 2 | 0 | 27-Mar-15 A | 02-Apr-15 A | |
| L1L-8150 | Plumbing rough-in at die wall (Bar) | 4 | 0 | 27-Mar-15 A | 31-Mar-15 A | |
| CN-1000 | Install exterior canopies - steel | 5 | 0 | 27-Mar-15 A | 01-Apr-15 A | |
| L03-8682 | Install waterproofing and protection layer | 3 | 0 | 27-Mar-15 A | 02-Apr-15 A | |
| L1B-8174 | Complete grease duct insulation & inspect at Prefunc | 5 | 0 | 27-Mar-15 A | 27-May-15 A | |
| L17-7046 | Field mesaure and fabricate vending countertops (OF | 10 | 0 | 27-Mar-15 A | 28-Apr-15 A | |
| CO-7230 | Cx - TAB - Air Balancing - Tower | 15 | 0 | 30-Mar-15 A | 10-Apr-15 A | |
| CO-7141 | Install Fire Alarm Devices & Map to Panel - Podium | 5 | 0 | 30-Mar-15 A | 17-Apr-15 A | |
| MPT-1094 | Caulking - Elevation 32 (south elevation, east of man | 10 | 0 | 30-Mar-15 A | 10-Apr-15 A | |
| MPT-1096 | Caulking - Elevation 33/34 (east elevation, south end | 10 | 0 | 30-Mar-15 A | 10-Apr-15 A | |
| I-6012 | Core drill & install new floor drain and piping | 2 | 0 | 30-Mar-15 A | 31-Mar-15 A | |
| CM-1016b | CM - Owner FF&E "Build-Out" - Floors 10 & 11 | 7 | 0 | 30-Mar-15 A | 05-Apr-15 A | |
| LL2-2110 | Restore epoxy flooring at dryer location | 5 | 0 | 30-Mar-15 A | 03-Apr-15 A | |
| I-1204 | Finish carpentry/millwork at Concierge Lounge | 5 | 0 | 31-Mar-15 A | 07-Apr-15 A | |
| LL1-8130 | Install base | 3 | 0 | 31-Mar-15 A | 03-Apr-15 A | |
| L1L-8138 | Flooring - epoxy floor (Bar) | 5 | 0 | 31-Mar-15 A | 03-Apr-15 A | |
| L1L-8280 | Install Peter Glassford art wall | 5 | 0 | 31-Mar-15 A | 03-Apr-15 A | |
| LL1-Z2-8144 | Install doors & hardware at corridors | 2 | 0 | 31-Mar-15 A | 01-Apr-15 A | |
| L1K-8212 | Lighting & electrical trim at ceiling | 2 | 0 | 31-Mar-15 A | 01-Apr-15 A | |
| L1L-8304 | Fire alarm trim (speaker strobe & smoke detector bas | 3 | 0 | 31-Mar-15 A | 31-Mar-15 A | |

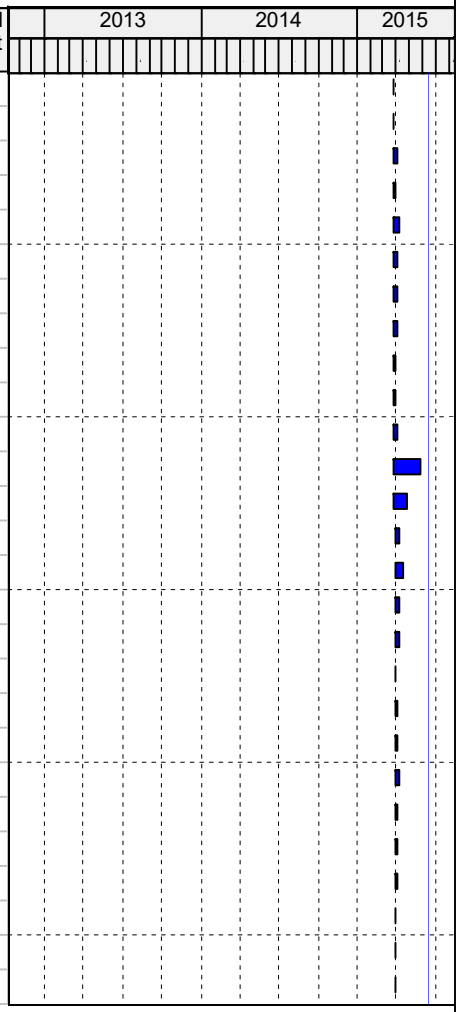



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8669 | Install anchor bolts for trench drain | 1 | 0 | 31-Mar-15 A | 31-Mar-15 A | |
| L1B-8178 | Complete framing & MEP at Prefunction 1 south end | 3 | 0 | 31-Mar-15 A | 02-Apr-15 A | |
| CO-7102T | Cx - DDC Point-To-Point - Central Plant [DELETED] | 5 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| L03-7044 | Finish carpentry/millwork - Vending/Guest Laundry Ca | 1 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7132 | Cx - DDC Point-To-Point - Ballroom VAV [DELETED] | 4 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7134 | Cx - DDC Point-To-Point - Ballroom RTU (2) [DELETEI | 2 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7402 | Cx - FPT - Central Plant [DELETED] | 2 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7406 | Cx - FPT - MUA, RTU, VAV and Exhaust Fansm [DEL | 5 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7408 | Cx - FPT - Garage Exhaust Fans [DELETED] | 1 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| CO-7410 | Cx - FPT - Misc Equipment [DELETED] | 4 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| MPT-1118 | Cap metal - Pool terrace [DELETED, INCLUDED IN G | 3 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| MPT-1120 | Cap metal at L12 Terrace [DELETED, INCLUDED IN I | 2 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| MPP-1004 | Pool Area cornice metal | 10 | 0 | 01-Apr-15 A | 21-May-15 A | |
| L03-8622 | HVAC trim at Pool | 2 | 0 | 01-Apr-15 A | 01-Apr-15 A | |
| LL2-2102 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 01-Apr-15 A | 06-Apr-15 A | |
| L1BOH2C-6026 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 01-Apr-15 A | 21-Apr-15 A | |
| L1L-8140a | Install 9-wood ceiling - south of Grid K | 4 | 0 | 01-Apr-15 A | 06-Apr-15 A | |
| CO-7116.1 | Smoke Control Equipment Pre-Testing (Fans & Dampı | 18 | 0 | 01-Apr-15 A | 15-May-15 A | |
| L02-8158 | Ceiling grid at north half | 3 | 0 | 02-Apr-15 A | 22-May-15 A | |
| L03-8206a | Flooring - carpet at corridors (E-W leg) | 2 | 0 | 02-Apr-15 A | 03-Apr-15 A | |
| I-6014 | Install temporary partition at corridor | 1 | 0 | 02-Apr-15 A | 02-Apr-15 A | |
| L1L-8320 | Paint, above 9-wood ceiling | 2 | 0 | 03-Apr-15 A | 06-Apr-15 A | |
| CO-7104T.1 | Fire Alarm/Smoke Control Pre-Functional Testing - To\ | 10 | 0 | 06-Apr-15 A | 17-Apr-15 A | |
| L1BOH2-8116 | Finish carpentry/millwork | 5 | 0 | 06-Apr-15 A | 06-Apr-15 A | |
| LL1-Z3-FCC38 | Final clean and punch list at FCC | 3 | 0 | 06-Apr-15 A | 07-Apr-15 A | |
| MPT-1074 | Tower Sign, South (El 32) | 5 | 0 | 06-Apr-15 A | 08-Apr-15 A | |
| L1L-8130 | Install bar and back bar | 10 | 0 | 06-Apr-15 A | 21-Apr-15 A | |

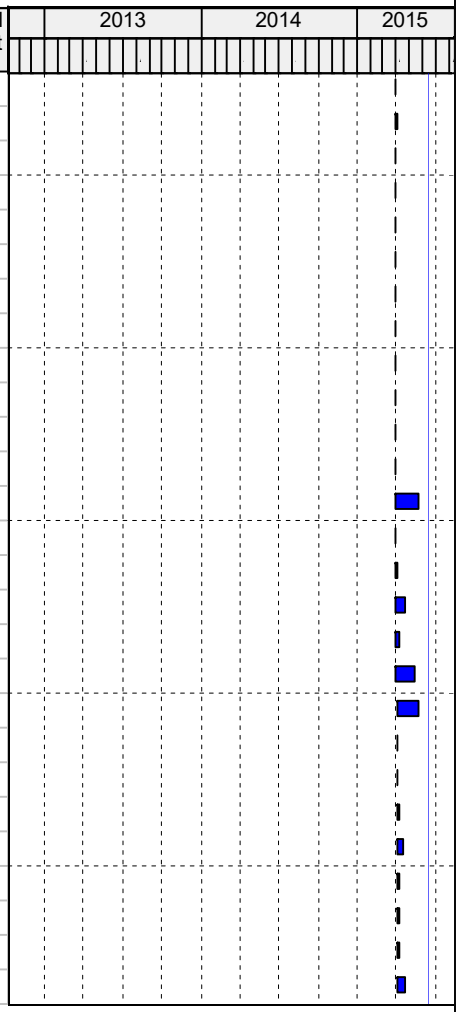



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8232 | Wall coverings - vinyl | 5 | 0 | 06-Apr-15 A | 14-Apr-15 A | |
| L1B-8142 | Paint, prime & first coat finish walls & ceilings at corrid | 2 | 0 | 06-Apr-15 A | 10-Apr-15 A | |
| L1B-8162 | Install doors & hardware at corridors | 2 | 0 | 06-Apr-15 A | 07-Apr-15 A | |
| L1L-8206a | Lighting & elecrical trim at ceilings - south of Grid K | 2 | 0 | 06-Apr-15 A | 06-Apr-15 A | |
| CM-1016e | CM - Owner FF+E "Build-Out" - Floors 12 & 14 | 7 | 0 | 06-Apr-15 A | 12-Apr-15 A | |
| SW-2050 | Street - Grind and overlay | 5 | 0 | 06-Apr-15 A | 09-Apr-15 A | |
| CN-1004 | Field measure & fabricate canopy glass | 15 | 0 | 06-Apr-15 A | 29-May-15 A | |
| CO-7139.2 | Install Fire Alarm Devices & Map to Panel - Tower Lev | 2 | 0 | 06-Apr-15 A | 08-Apr-15 A | |
| I-7100 | Resolve dryer duct issue | 10 | 0 | 06-Apr-15 A | 07-May-15 A | |
| I-7102 | TPAP box impact | 5 | 0 | 06-Apr-15 A | 08-May-15 A | |
| L03-8628 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L02-8140 | Lighting & electrical trim at south half | 2 | 0 | 07-Apr-15 A | 14-Apr-15 A | |
| L1L-8234 | Fire sprinkler trim at ceilings | 1 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8236 | Lighting & electrical trim at ceilings | 2 | 0 | 07-Apr-15 A | 16-Apr-15 A | |
| L1L-8262 | Fire sprinkler trim at ceilings | 1 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8264 | Lighting & electrical trim at ceilings | 3 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8266 | HVAC drops/trim at celing | 2 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8284 | Install handrails | 2 | 0 | 07-Apr-15 A | 08-Apr-15 A | |
| L1L-8298 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8318 | Install 9-wood ceiling at Sitting Area | 3 | 0 | 07-Apr-15 A | 14-Apr-15 A | |
| L1L-8204a | HVAC trim at ceiling - south of Grid K | 1 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8112a | Fire sprinkler trim - south of Grid K | 1 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| I-1206 | Install ceiling at Concierge Lounge (BOK) | 4 | 0 | 08-Apr-15 A | 09-Apr-15 A | |
| L1L-8238 | HVAC drops/trim at celing | 1 | 0 | 08-Apr-15 A | 08-Apr-15 A | |
| L1K-8128b | Ansul system final connections | 10 | 0 | 10-Apr-15 A | 15-May-15 A | |
| I-7104 | Resolve HHP issue (RFI 964) | 10 | 0 | 13-Apr-15 A | 04-May-15 A | |
| L1B-8128 | Install base at Ballrooms | 5 | 0 | 13-Apr-15 A | 17-Apr-15 A | |

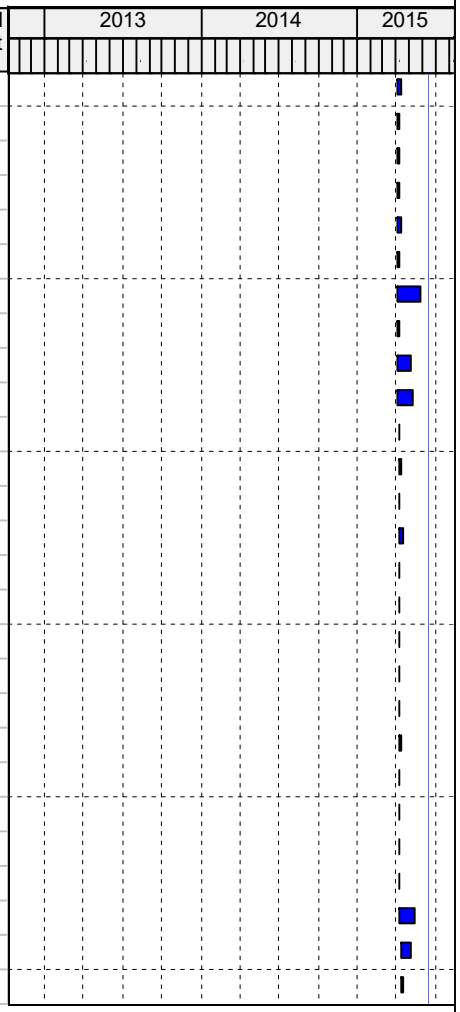



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| SW-2122 | Zone 1 - Install landscaping & irrigation | 15 | 0 | 13-Apr-15 A | 23-Apr-15 A | |
| SW-2218 | Zone 2 - Install landscaping & irrigation | 15 | 0 | 13-Apr-15 A | 22-Apr-15 A | |
| CO-7136 | Cx - DDC Point-To-Point | 10 | 0 | 13-Apr-15 A | 27-May-15 A | |
| SW-2330 | Zone 3 - Landscaping & irrigation | 15 | 0 | 13-Apr-15 A | 27-Apr-15 A | |
| LL1-Z3-8158 | Install toilet partitions | 2 | 0 | 13-Apr-15 A | 14-Apr-15 A | |
| L1L-8118a | Fire alarm trim (spreaker strobe & smoke detector bas | 1 | 0 | 13-Apr-15 A | 13-Apr-15 A | |
| CM-1016f | CM - Owner FF+E "Build-Out" - Floors 15 & 16 | 7 | 0 | 13-Apr-15 A | 19-Apr-15 A | |
| CO-7231 | Cx - TAB - Air Balancing - Podium | 10 | 0 | 13-Apr-15 A | 15-May-15 A | |
| CO-7104T.3 | Compile/Certify/Accept TAB Report - Tower | 3 | 0 | 13-Apr-15 A | 15-Apr-15 A | |
| I-7200 | Owner approve pricing fo mirrors | 5 | 0 | 13-Apr-15 A | 21-Apr-15 A | |
| I-7250 | Resolve ceiling height issue at corridors | 5 | 0 | 13-Apr-15 A | 29-Apr-15 A | |
| L1BOH2-8112 | Fire sprinkler drops/trim at ceiling | 1 | 0 | 14-Apr-15 A | 14-Apr-15 A | |
| L17-8140 | Complete window sills | 1 | 0 | 14-Apr-15 A | 14-Apr-15 A | |
| L1K-8202 | Ceiling grid at Janitorial | 1 | 0 | 14-Apr-15 A | 14-Apr-15 A | |
| L1L-8242 | Finish carpentry/millwork (including front desk) | 4 | 0 | 14-Apr-15 A | 08-May-15 A | |
| L1L-8286 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 14-Apr-15 A | 14-Apr-15 A | |
| L1K-8222 | Install toilet partitions | 2 | 0 | 14-Apr-15 A | 15-Apr-15 A | |
| LL1-Z3-FCC22 | Final inspections by CoB and Fire Marshall (DELETEI | 2 | 0 | 15-Apr-15 A | 15-Apr-15 A | |
| LL1-Z3-FCC40 | Install Knox Box at FCC | 1 | 0 | 15-Apr-15 A | 15-Apr-15 A | |
| L1B-8146 | HVAC drops/trim at corridors | 2 | 0 | 15-Apr-15 A | 30-Apr-15 A | |
| L1B-8148 | Lighting & electrical trim at corridors | 2 | 0 | 15-Apr-15 A | 29-Apr-15 A | |
| L02-8156 | Install doors & hardware at north half | 3 | 0 | 15-Apr-15 A | 11-May-15 A | |
| L02-8166 | Fire sprinkler trim at north half | 2 | 0 | 15-Apr-15 A | 01-Jun-15 A | |
| SW-2068 | Street - Striping | 2 | 0 | 15-Apr-15 A | 15-Apr-15 A | |
| I-7230 | Owner provide authroization for additional backing | 2 | 0 | 15-Apr-15 A | 16-Apr-15 A | |
| L1L-8122 | Electrical trim & finish at bar (bar area final connectior | 2 | 0 | 16-Apr-15 A | 12-May-15 A | |
| L02-8114 | Floor prep at south half | 2 | 0 | 16-Apr-15 A | 17-Apr-15 A | |

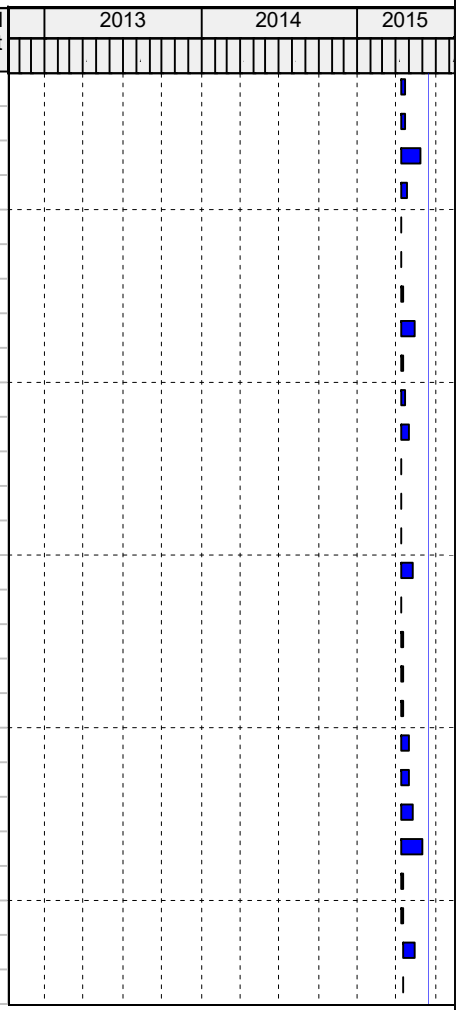



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| I-7210 | Owner deliver wood flooring (to Spectra's office) | 5 | 0 | 16-Apr-15 A | 28-Apr-15 A | |
| I-7222 | Fabricate and deliver bar countertops | 10 | 0 | 16-Apr-15 A | 13-May-15 A | |
| I-7224 | Owner approve change order for revised VWC installa | 3 | 0 | 16-Apr-15 A | 29-Apr-15 A | |
| L1B-8144 | Wall coverings - vinyl at corridors | 3 | 0 | 17-Apr-15 A | 11-May-15 A | |
| L02-8168 | Floor prep at north half | 1 | 0 | 17-Apr-15 A | 17-Apr-15 A | |
| LL2-8156 | Remove job shacks | 1 | 0 | 17-Apr-15 A | 24-Apr-15 A | |
| I-7220 | Owner provide direction on sink change and custom t | 10 | 0 | 17-Apr-15 A | 16-May-15 A | |
| L03-8648 | Pool Equipment Room - Install 2-hr shaft | 1 | 0 | 18-Apr-15 A | 18-Apr-15 A | |
| CM-1016a | CM - Owner FF+E "Build-Out" - Floors 3 & 17 | 7 | 0 | 20-Apr-15 A | 24-Apr-15 A | |
| LL2-8152 | Clear out and clean parking area | 10 | 2 | 20-Apr-15 A | 16-Jun-15 | 2 |
| L1L-8159 | Owner approve pricing for TV feature wall installation | 5 | 0 | 20-Apr-15 A | 29-Apr-15 A | |
| I-7270 | Pool Equipment Room - Re-design & layout equipme | 10 | 2 | 20-Apr-15 A | 16-Jun-15 | 7 |
| I-7400 | Owner approve pricing for revised street signage & pr | 10 | 2 | 20-Apr-15 A | 16-Jun-15 | 2 |
| I-7202 | South Door - Frame Soffit | 1 | 0 | 21-Apr-15 A | 21-Apr-15 A | |
| RF-4066 | Pool Green Roof - Install decorative metal railing | 3 | 0 | 22-Apr-15 A | 23-Apr-15 A | |
| L02-8150 | Install doors & hardware at Locker Rooms | 1 | 0 | 22-Apr-15 A | 26-May-15 A | |
| LL2-8106b | Pinned insulation at ramp at Garage & dry shack area | 5 | 0 | 22-Apr-15 A | 28-Apr-15 A | |
| I-7204 | South Door - GWB at Soffit | 4 | 0 | 22-Apr-15 A | 29-Apr-15 A | |
| L1K-8342 | Final connections at walk-in cooler/freezer | 2 | 0 | 23-Apr-15 A | 15-May-15 A | |
| L1K-8125 | Floor prep | 1 | 0 | 23-Apr-15 A | 23-Apr-15 A | |
| L02-8152 | Flooring - VCT at south half | 10 | 0 | 23-Apr-15 A | 07-May-15 A | |
| L02-8170 | Flooring - VCT at north half | 10 | 0 | 23-Apr-15 A | 10-Jun-15 A | |
| LL1-8116a | Install countertops (owner-furnished) | 2 | 0 | 24-Apr-15 A | 30-Apr-15 A | |
| CO-7264 | Cx - Start-Up - Lobby Trane TRU (2) | 2 | 0 | 27-Apr-15 A | 28-Apr-15 A | |
| L1L-8239 | Floor prep | 2 | 0 | 27-Apr-15 A | 28-Apr-15 A | |
| L1B-8150 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 27-Apr-15 A | 28-Apr-15 A | |
| L1B-8152 | Fire sprinkler drops/trim at corridors | 1 | 0 | 27-Apr-15 A | 27-Apr-15 A | |

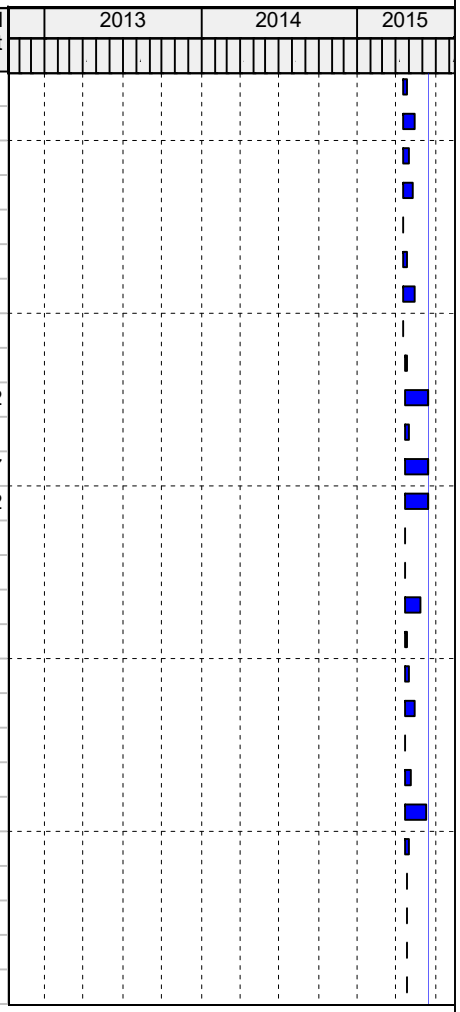



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-8152 | Measure & fabricate mirrors | 10 | 0 | 27-Apr-15 A | 05-May-15 A | |
| CM-1016g | CM - Owner FF+E "Build-Out" Complete All Floors | 7 | 0 | 27-Apr-15 A | 29-May-15 A | |
| I-7460 | Complete ACT engineering | 5 | 0 | 27-Apr-15 A | 14-May-15 A | |
| CO-7160 | Generator - Cx generator/owner training | 3 | 0 | 28-Apr-15 A | 28-Apr-15 A | |
| L1L-8240 | Flooring - tile & base | 6 | 0 | 28-Apr-15 A | 08-May-15 A | |
| L1B-8202 | Wall coverings - vinyl at Ballrooms | 5 | 0 | 29-Apr-15 A | 07-May-15 A | |
| L02-8154 | Wall coverings - vinyl at north half | 3 | 0 | 29-Apr-15 A | 01-Jun-15 A | |
| L17-7048 | Install vending countertops (OFM) - L4-L17 | 2 | 0 | 29-Apr-15 A | 29-Apr-15 A | |
| I-7206 | South Door - Paint Soffit | 1 | 0 | 29-Apr-15 A | 29-Apr-15 A | |
| I-7212 | Deliver flooring to job site & wood flooring acclimate | 7 | 0 | 29-Apr-15 A | 07-May-15 A | |
| MPT-1084 | Caulking - Hi-roof cornice metal | 5 | 0 | 30-Apr-15 A | 01-May-15 A | |
| MPP-1018 | Elevation A/B/C (Porte Cochere wall panels) | 2 | 0 | 30-Apr-15 A | 20-May-15 A | |
| LL1-Z2-8116a | Install countertops (owner-furnished) | 1 | 0 | 30-Apr-15 A | 01-May-15 A | |
| I-7208 | South Door - Install wood panels | 1 | 0 | 30-Apr-15 A | 30-Apr-15 A | |
| L1L-8160 | Install TV feature wall panels/screens | 3 | 0 | 30-Apr-15 A | 07-May-15 A | |
| I-7252 | Reinstall ceiling grild at south half | 3 | 0 | 30-Apr-15 A | 07-May-15 A | |
| I-7510 | Relocate MUA 7 damper (RFI 988) | 5 | 0 | 30-Apr-15 A | 07-May-15 A | |
| L03-8672 | Prep & pour pool topping slab [DELETED] | 2 | 0 | 01-May-15 A | 01-May-15 A | |
| SW-2232 | Zone 2 - Replace luminaire north of 3rd (DELETED) | 1 | 0 | 01-May-15 A | 01-May-15 A | |
| SW-2328 | Zone 3 - Pull wire and install light poles (DELETED) | 5 | 0 | 01-May-15 A | 01-May-15 A | |
| SW-2056 | Zone 4 - Pull wire and replace luminaires on 110th (DI | 5 | 0 | 01-May-15 A | 01-May-15 A | |
| I-1210 | Floor prep | 2 | 0 | 01-May-15 A | 06-May-15 A | |
| I-7802 | Owner approve site lighting change order | 25 | 0 | 01-May-15 A | 12-Jun-15 A | |
| I-7240 | RFI 989 - Modify front desk for ADA | 10 | 0 | 01-May-15 A | 14-May-15 A | |
| CM-1022 | Podium - "Clean/Punch" Complete - All Floors, All Zon | 0 | 0 | | 01-May-15 A | |
| L17-7032 | Flooring - VCT (x42) | 1 | 0 | 04-May-15 A | 04-May-15 A | |
| MPP-1040 | Caulking - Pool Area & Ballroom cornice metal | 3 | 0 | 04-May-15 A | 29-May-15 A | |

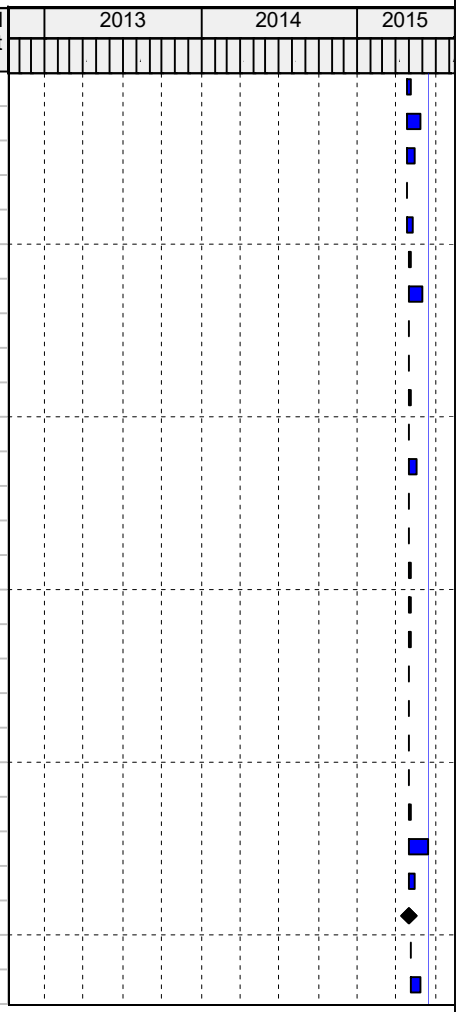



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8138 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 04-May-15 A | 19-Jun-15 | 7 |
| LL3-8138 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 5 | 04-May-15 A | 19-Jun-15 | 7 |
| RF-4074 | Pool Green Roof - Install parapet coping | 6 | 0 | 04-May-15 A | 09-May-15 A | |
| I-7226 | Install revised vinyl wallcoverings | 3 | 0 | 04-May-15 A | 15-May-15 A | |
| L1B-8198 | Paint at East Service Corridor | 3 | 0 | 04-May-15 A | 06-May-15 A | |
| I-7228 | Die wall correction notice - resolve (RFI 982) | 5 | 0 | 04-May-15 A | 21-May-15 A | |
| I-7236 | Owner provide remaining Kitchen equipment | 10 | 0 | 04-May-15 A | 14-May-15 A | |
| I-7108 | Restore grid ceiling | 1 | 0 | 05-May-15 A | 05-May-15 A | |
| I-7110 | Relocate lighting | 1 | 0 | 05-May-15 A | 05-May-15 A | |
| I-1202 | Flooring - tile at Concierge Lounge | 5 | 0 | 06-May-15 A | 11-May-15 A | |
| LL1-Z3-8146 | Install restroom accessories | 2 | 0 | 06-May-15 A | 28-May-15 A | |
| LL1-8144 | Install mirrors | 3 | 0 | 06-May-15 A | 08-May-15 A | |
| L1B-8154 | Finish carpentry/millwork at corridors | 2 | 0 | 06-May-15 A | 11-May-15 A | |
| L1B-8156 | Install base at corridors | 5 | 0 | 06-May-15 A | 18-May-15 A | |
| MPP-1060 | Install alcoves, south (paint) | 1 | 0 | 06-May-15 A | 11-Jun-15 A | |
| RF-4076 | Pool Green Roof - Install decorative glass | 2 | 0 | 06-May-15 A | 07-May-15 A | |
| I-7112 | Relocate sprinklers | 1 | 0 | 06-May-15 A | 06-May-15 A | |
| I-7114 | Ceiling cover inspection failure - laundry ironer - resol\ | 5 | 0 | 06-May-15 A | 12-Jun-15 A | |
| RF-4078 | TR - Terrace Roof - Install parapet coping | 6 | 0 | 07-May-15 A | 08-May-15 A | |
| L1BOH2-8201 | Paint, final coat & touch-up | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1BOH2-8118 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| LL1-8146 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| LL1-8148 | Complete acoustical ceiling tile | 2 | 0 | 07-May-15 A | 09-Jun-15 A | |
| LL1-Z3-8152 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1B-8136 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1K-8156 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1K-8158 | Complete paint final coat & touch-up | 2 | 0 | 07-May-15 A | 08-May-15 A | |

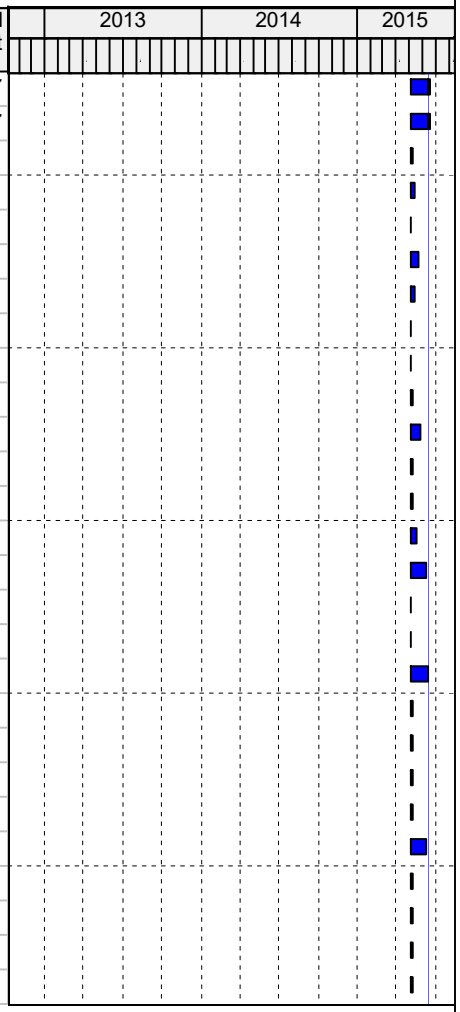



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8244 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1L-8268 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| LL1-8188 | Complete paint final coat & touch-up | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| LL1-Z3-8150 | Complete paint final coat & touch-up | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| LL1-Z3-8154 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1L-8203 | Complete MEP trim | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1L-8288 | Paint, final coat & touch-up | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1L-8300 | Paint, final coat & touch-up | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| MPP-1050 | Columns at Porte Cochere | 4 | 0 | 07-May-15 A | 09-Jun-15 A | |
| RF-4080 | TR - Terrace Roof - Install decorative glass | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| L1B-8210 | Ceiling grind at East Service Corridor | 4 | 0 | 07-May-15 A | 11-May-15 A | |
| L1L-8123 | Floor prep - north of Grid K | 2 | 0 | 08-May-15 A | 09-May-15 A | |
| LL1-Z3-8156 | Install countertops at restrooms | 2 | 0 | 08-May-15 A | 27-May-15 A | |
| L1L-8123a | Floor prep - south of Grid K | 2 | 0 | 08-May-15 A | 09-May-15 A | |
| I-7106 | Restore dryer wall & FRP | 5 | 0 | 08-May-15 A | 18-May-15 A | |
| RF-4068 | Pool Green Roof - Install American Hydrotech assemI | 3 | 0 | 11-May-15 A | 13-May-15 A | |
| RF-4070 | TR - Terrace Roof - Install American Hydrotech assem | 3 | 0 | 11-May-15 A | 13-May-15 A | |
| L02-8172 | Finish carpentry/millwork at north half | 1 | 0 | 11-May-15 A | 13-May-15 A | |
| L1L-8124b | Flooring - wood - south of Grid K | 4 | 0 | 11-May-15 A | 22-May-15 A | |
| I-7232 | Install additional backing (RFI 976) | 3 | 0 | 11-May-15 A | 14-May-15 A | |
| L1B-8212 | MEP drops/trim to grid at East Service Corridor (incl. i | 4 | 0 | 11-May-15 A | 13-May-15 A | |
| L1L-8123b | Floor prep - bar | 1 | 0 | 11-May-15 A | 11-May-15 A | |
| MPP-1038 | Podium Signs, West | 1 | 0 | 12-May-15 A | 12-May-15 A | |
| L1K-8220 | Install countertops in restrooms | 2 | 0 | 12-May-15 A | 27-May-15 A | |
| I-7810 | Replace vanity top in Women's restroom | 1 | 0 | 12-May-15 A | 15-May-15 A | |
| I-7812 | Replace vanity top in Women's restroom | 1 | 0 | 12-May-15 A | 20-May-15 A | |
| L1L-8120 | Plumbing fixtures & trim (Bar) | 2 | 0 | 13-May-15 A | 14-May-15 A | |

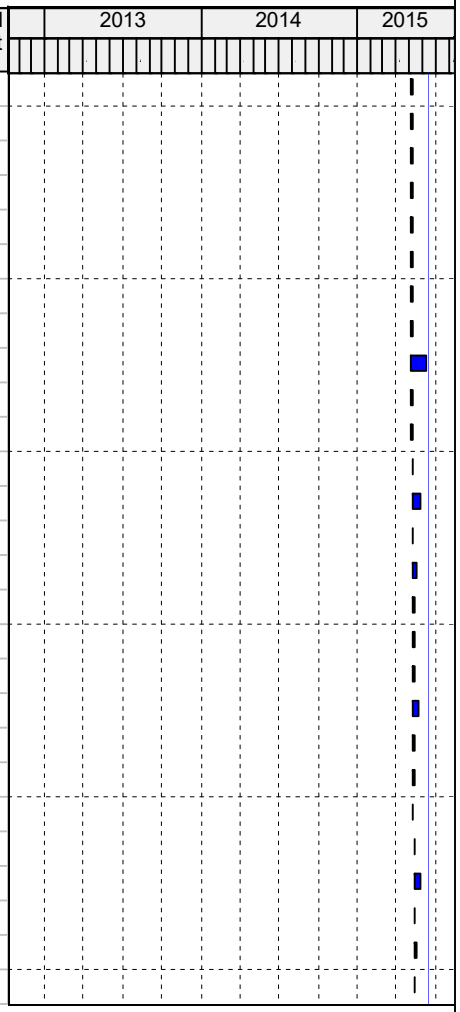



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CO-7172 | Compile/Certify/Accept TAB Report - Podium | 3 | 0 | 13-May-15 A | 15-May-15 A | |
| I-7500 | Finishes at TPA/TPB boxes | 6 | 0 | 13-May-15 A | 26-May-15 A | |
| LL1-Z3-8162 | Install sinks at Restrooms | 2 | 0 | 14-May-15 A | 28-May-15 A | |
| L03-8690 | Pool Equipment Room - Install epoxy flooring | 3 | 0 | 14-May-15 A | 16-May-15 A | |
| L1B-8216 | Floor prep at East Service Corridor | 1 | 0 | 14-May-15 A | 14-May-15 A | |
| L1B-8218 | Flooring - VCT at East Service Corridor | 2 | 0 | 14-May-15 A | 15-May-15 A | |
| I-7462 | Modify ACT grid (including inspection) | 2 | 0 | 14-May-15 A | 15-May-15 A | |
| I-7340 | Install countertops | 2 | 0 | 14-May-15 A | 26-May-15 A | |
| LL2-2050 | Laundry Room equipment final connections (MEP) | 3 | 0 | 15-May-15 A | 20-May-15 A | |
| I-1214 | Install base | 2 | 0 | 15-May-15 A | 18-May-15 A | |
| I-7234 | Install kitchen shelving (by owner) | 2 | 0 | 15-May-15 A | 15-May-15 A | |
| I-7238 | Resolve equipment power conflicts (RFI 1013) | 2 | 1 | 15-May-15 A | 15-Jun-15 | 4 |
| I-7242 | Field measure and fabricate front desk top | 10 | 0 | 15-May-15 A | 26-May-15 A | |
| L1B-8196 | Install acoustical ceiling tile | 2 | 0 | 17-May-15 A | 18-May-15 A | |
| I-7116 | Finishes at TPA/TPB boxes | 2 | 0 | 17-May-15 A | 05-Jun-15 A | |
| L1K-8208 | Install restroom accessories | 2 | 0 | 18-May-15 A | 28-May-15 A | |
| L1K-8154 | Complete acoustical ceiling tile | 2 | 0 | 18-May-15 A | 19-May-15 A | |
| L1B-8129 | Floor prep | 2 | 0 | 18-May-15 A | 19-May-15 A | |
| I-7880 | Procure revised rope lights | 3 | 1 | 18-May-15 A | 15-Jun-15 | 2 |
| CO-7138 | Elevator Finals with AHJ | 6 | 0 | 19-May-15 A | 27-May-15 A | |
| MPP-1056 | Caulking - Porte Cochere walls & columns | 3 | 0 | 19-May-15 A | 10-Jun-15 A | |
| L1K-8224 | Install sinks at restrooms | 2 | 0 | 19-May-15 A | 28-May-15 A | |
| EL-1240 | Elev 1&2 - Final elevator inspection | 2 | 0 | 19-May-15 A | 20-May-15 A | |
| L1L-8124c | Flooring - tile - in front of bar | 4 | 0 | 19-May-15 A | 28-May-15 A | |
| L1L-8322 | Install base | 2 | 0 | 19-May-15 A | 20-May-15 A | |
| L02-8142 | Ceiling grid at Locker Rooms | 3 | 0 | 20-May-15 A | 22-May-15 A | |
| L1L-8308 | Floor (stair) prep | 1 | 0 | 20-May-15 A | 20-May-15 A | |

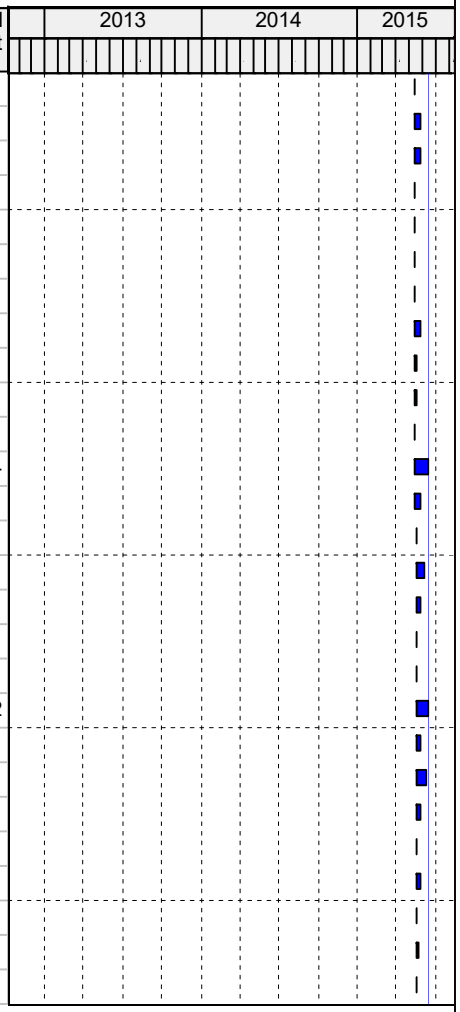



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1L-8158 | Install bar countertops | 2 | 0 | 20-May-15 A | 22-May-15 A | |
| L1L-8278 | Flooring - tile at stair treads | 4 | 0 | 21-May-15 A | 05-Jun-15 A | |
| L1L-8162 | Install quartz base at TV feature wall | 3 | 0 | 21-May-15 A | 22-May-15 A | |
| I-7248 | Install beverage lines (by owner) | 5 | 0 | 22-May-15 A | 12-Jun-15 A | |
| L1BOH2-8124a | Install base | 1 | 0 | 26-May-15 A | 26-May-15 A | |
| L02-8160 | HVAC drops/trim at north half | 2 | 0 | 26-May-15 A | 29-May-15 A | |
| L02-8162 | Lighting & electrical trim at north half | 2 | 0 | 26-May-15 A | 29-May-15 A | |
| CO-7152 | Final Inspection - Plumbing | 10 | 5 | 26-May-15 A | 19-Jun-15 | 1 |
| L1L-8166 | Install bar front and ceramic tile | 4 | 0 | 26-May-15 A | 10-Jun-15 A | |
| CO-7124 | Final Inspection - Building Department | 18 | 9 | 27-May-15 A | 25-Jun-15 | 0 |
| L02-8145 | MEP drops to framed ceiling (including inspections) | 2 | 0 | 27-May-15 A | 01-Jun-15 A | |
| MPP-1064 | Install column at Pool | 1 | 0 | 27-May-15 A | 27-May-15 A | |
| CO-7150 | Final Inspection - Electrical | 10 | 5 | 27-May-15 A | 19-Jun-15 | 1 |
| I-7254 | Modify front desk and stone top | 1 | 0 | 27-May-15 A | 29-May-15 A | |
| I-7256 | Modify stone at feature wall base | 1 | 0 | 27-May-15 A | 08-Jun-15 A | |
| CO-7154 | Final Inspection - Mechanical | 10 | 5 | 28-May-15 A | 19-Jun-15 | 1 |
| L1L-8124a | Install base | 2 | 0 | 28-May-15 A | 08-Jun-15 A | |
| L02-8164 | Fire alarm trim (speaker/strobe & smoke detector bas | 2 | 0 | 28-May-15 A | 01-Jun-15 A | |
| L1L-8296 | Install walk-off mat (including floor prep) | 3 | 0 | 28-May-15 A | 09-Jun-15 A | |
| L1BOH2-8140 | Acoustical ceiling tile | 2 | 0 | 01-Jun-15 A | 09-Jun-15 A | |
| L1BOH2-8123 | Floor prep | 1 | 0 | 01-Jun-15 A | 01-Jun-15 A | |
| LL2-8162 | Owner clear out parking area for cleaning & striping | 15 | 2 | 01-Jun-15 A | 16-Jun-15 | 3 |
| L1BOH2-8128 | Flooring - carpet | 3 | 0 | 02-Jun-15 A | 02-Jun-15 A | |
| I-7244 | Install front desk top | 1 | 0 | 02-Jun-15 A | 02-Jun-15 A | |
| I-7246 | Complete connections at front desk | 1 | 0 | 03-Jun-15 A | 03-Jun-15 A | |
| CN-1002 | Install exterior canopies - glass | 3 | 1 | 04-Jun-15 A | 15-Jun-15 | 5 |
| L1B-8220 | Paint at Prefunction 2 | 2 | 0 | 04-Jun-15 A | 04-Jun-15 A | |

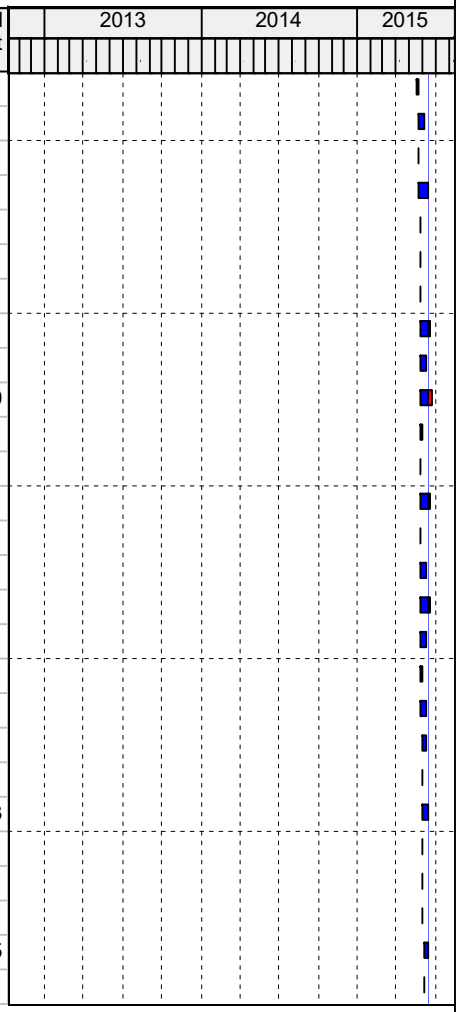



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-8140 | Final Cleaning - Garage, North Half | 1 | 0 | 05-Jun-15 A | 05-Jun-15 A | |
| L1B-8180 | HVAC drops/trim at Prefunction 2 | 2 | 0 | 08-Jun-15 A | 09-Jun-15 A | |
| L1B-8182 | Lighting & electrical trim at Prefunction 2 | 2 | 0 | 08-Jun-15 A | 09-Jun-15 A | |
| L1B-8184 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 08-Jun-15 A | 09-Jun-15 A | |
| LL3-8140 | Final Cleaning - Garage | 1 | 0 | 08-Jun-15 A | 08-Jun-15 A | |
| I-7804 | Procure NE 2nd luminaires | 10 | 5 | 08-Jun-15 A | 19-Jun-15 | 1 |
| LL2-8144 | Complete acoustical ceiling tile | 2 | 1 | 09-Jun-15 A | 15-Jun-15 | 6 |
| CO-7148 | Final Inspection - Utilities | 3 | 0 | 09-Jun-15 A | 09-Jun-15 A | |
| L1B-8188 | Finish carpentry/millwork at Prefunction 2 | 2 | 0 | 09-Jun-15 A | 12-Jun-15 A | |
| L1L-8164 | Complete TV feature wall panels/screens | 2 | 0 | 09-Jun-15 A | 10-Jun-15 A | |
| LL4-8144 | Striping, North Half (incl. inspection) | 2 | 0 | 09-Jun-15 A | 10-Jun-15 A | |
| LL3-8142 | Striping (incl. inspection) | 2 | 0 | 09-Jun-15 A | 10-Jun-15 A | |
| L02-8182 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 2 | 10-Jun-15 A | 18-Jun-15 | 8 |
| L1B-8168 | Wall coverings - vinyl at Prefunction 2 | 2 | 0 | 10-Jun-15 A | 11-Jun-15 A | |
| L1B-8186 | Fire sprinkler drops/trim at Prefunction 2 | 1 | 0 | 10-Jun-15 A | 10-Jun-15 A | |
| L1B-8190 | Install base at Prefunction 2 | 2 | 0 | 10-Jun-15 A | 12-Jun-15 A | |
| L1B-8166 | Install operable partition doors | 2 | 0 | 10-Jun-15 A | 11-Jun-15 A | |
| L1L-8324 | Install stair skirt | 2 | 2 | 12-Jun-15 A | 16-Jun-15 | 5 |
| L1BOH2-8134 | Final Cleaning - Administrative | 5 | 5 | 15-Jun-15 | 19-Jun-15 | 5 |
| L02-8138 | Complete acoustical ceiling tile | 2 | 2 | 15-Jun-15 | 16-Jun-15 | 8 |
| SW-2228 | Install street lighting - All site zones | 2 | 2 | 15-Jun-15 | 16-Jun-15 | 4 |
| L1B-8160 | Floor prep | 2 | 2 | 15-Jun-15 | 16-Jun-15 | 2 |
| CO-7146 | Final Inspection - Clear & Grade | 5 | 5 | 15-Jun-15 | 19-Jun-15 | 1 |
| L1BOH2-8136 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 15-Jun-15 | 19-Jun-15 | 7 |
| LL1-8190 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 15-Jun-15 | 19-Jun-15 | 7 |
| LL1-Z2-8162 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 15-Jun-15 | 19-Jun-15 | 7 |
| LL1-Z3-8136 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 15-Jun-15 | 19-Jun-15 | 7 |

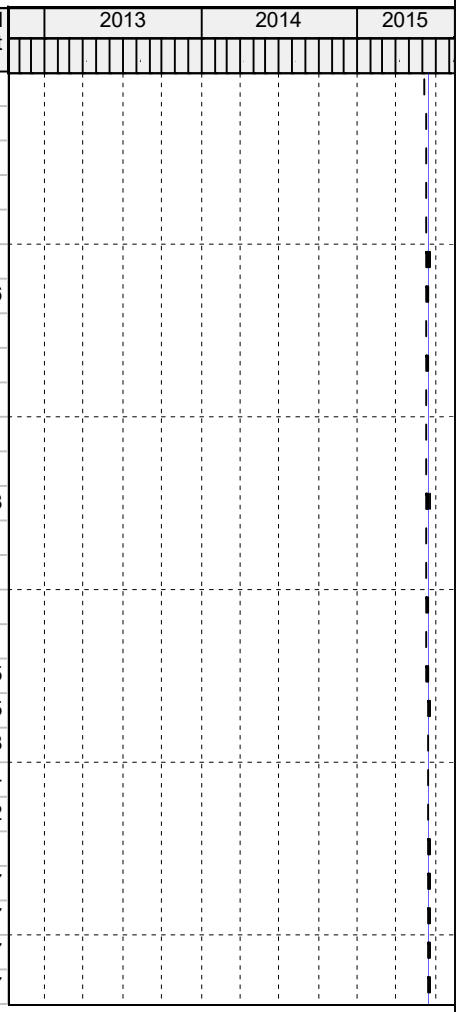



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8166 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 15-Jun-15 | 19-Jun-15 | 7 |
| I-1216 | Flooring - install carpet inserts | 2 | 2 | 15-Jun-15* | 16-Jun-15 | 5 |
| L1L-8168 | Flooring - install carpet inserts | 2 | 2 | 15-Jun-15 | 16-Jun-15 | 5 |
| LL4-8148 | Relocate laydown area | 2 | 2 | 15-Jun-15 | 16-Jun-15 | 1 |
| L1K-8128c | City of Bellevue Kitchen approval | 2 | 2 | 16-Jun-15 | 17-Jun-15 | 5 |
| I-7882 | Install revised rope lights | 2 | 2 | 16-Jun-15 | 17-Jun-15 | 2 |
| L1B-8130 | Flooring - VCT at A/V room | 2 | 2 | 17-Jun-15 | 18-Jun-15 | 3 |
| L1B-8158 | Flooring - carpet at south corridor & Prefunction 1 | 3 | 3 | 17-Jun-15 | 19-Jun-15 | 2 |
| L1L-8156 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 17-Jun-15 | 23-Jun-15 | 5 |
| SW-2070 | Street - Signage | 3 | 3 | 17-Jun-15 | 19-Jun-15 | 2 |
| L1B-8194 | Floor prep at Prefunction 2 | 1 | 1 | 17-Jun-15 | 17-Jun-15 | 4 |
| L03-8692 | Pool Equipment Room - Hang/tape GWB | 5 | 5 | 17-Jun-15 | 23-Jun-15 | 7 |
| LL4-8142 | Final Cleaning - Garage, South Half | 1 | 1 | 17-Jun-15 | 17-Jun-15 | 1 |
| LL2-8158 | Final Cleaning - Garage | 1 | 1 | 17-Jun-15 | 17-Jun-15 | 3 |
| CO-7156 | Final Inspection - Health Department (Kitchens) | 3 | 3 | 18-Jun-15 | 22-Jun-15 | 9 |
| CM-1018.1 | CM - Kitchen Burn-In & Training | 14 | 14 | 18-Jun-15 | 01-Jul-15 | 37 |
| I-7884 | Complete column light covers | 3 | 3 | 18-Jun-15 | 22-Jun-15 | 2 |
| LL4-8146 | Striping, South Half (incl. inspection) | 2 | 2 | 18-Jun-15 | 19-Jun-15 | 1 |
| LL2-8160 | Striping (incl. inspection) | 2 | 2 | 18-Jun-15 | 19-Jun-15 | 3 |
| L1BOH2-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 22-Jun-15 | 24-Jun-15 | 7 |
| L03-8670 | Complete trench drains at Pool (radius trench drain) | 2 | 2 | 22-Jun-15 | 23-Jun-15 | 0 |
| CO-7144 | Final Inspection - Transportation (Right-Of-Way) | 2 | 2 | 22-Jun-15 | 23-Jun-15 | 1 |
| LL2-8154 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 22-Jun-15 | 26-Jun-15 | 2 |
| L1B-8172 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 5 | 22-Jun-15 | 26-Jun-15 | 2 |
| L1B-8192 | Flooring - carpet at Prefunction 2 | 2 | 2 | 22-Jun-15 | 23-Jun-15 | 2 |
| L1L-8170 | Final Cleaning - Dining/Lounge/Bar, Lobby, Front Des | 5 | 5 | 22-Jun-15 | 26-Jun-15 | 5 |
| I-7806 | Install NE 2nd luminaires | 1 | 1 | 22-Jun-15 | 22-Jun-15 | 1 |

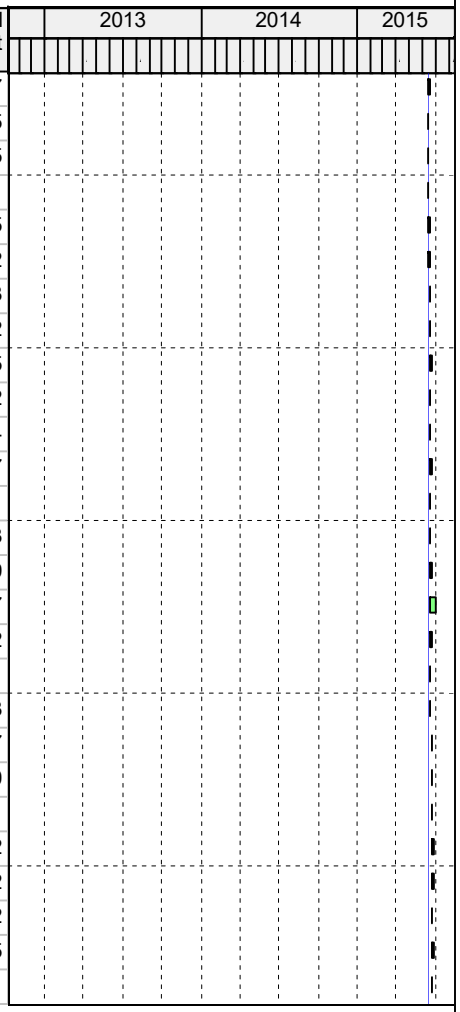


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-8688 | Pour pool topping slab | 2 | 2 | 24-Jun-15 | 25-Jun-15 | 0 |
| L03-8694 | Pool Equipment Room - Paint | 2 | 2 | 24-Jun-15 | 25-Jun-15 | 7 |
| L1BOH2-81214 | L1, Zone 3 Complete | 0 | 0 | | 24-Jun-15 | 7 |
| CO-7010 | TCO - Temporary Certificate of Occupancy | 0 | 0 | | 25-Jun-15* | 0 |
| L03-8674 | Complete storefront at Pool entry & install glazing | 2 | 2 | 26-Jun-15 | 29-Jun-15 | 6 |
| L03-8696 | Pool Equipment Room - Install pool equipment | 3 | 3 | 26-Jun-15 | 30-Jun-15 | 7 |
| LL2-8150 | LL2 Floor Complete | 0 | 0 | | 01-Jul-15 | 2 |
| L03-8640 | Prep and install pool plaster | 3 | 3 | 06-Jul-15 | 08-Jul-15 | 0 |
| L03-8618 | Ceramic tile at pool area | 8 | 8 | 09-Jul-15 | 20-Jul-15 | 0 |
| L03-8642 | Fill pool | 1 | 1 | 09-Jul-15 | 09-Jul-15 | 1 |
| L03-8644 | Connect, startup & adjust pool equipment | 10 | 10 | 10-Jul-15 | 23-Jul-15 | 1 |
| L03-8620 | Plumbing fixtures & trim at Pool | 2 | 2 | 21-Jul-15 | 22-Jul-15 | 0 |
| L03-8626 | Electrical trim & finish at Pool | 2 | 2 | 21-Jul-15 | 22-Jul-15 | 0 |
| L03-8630 | Install doors & hardware at Pool | 2 | 2 | 21-Jul-15 | 22-Jul-15 | 2 |
| L03-8638 | Install pool deck and ADA lift | 3 | 3 | 21-Jul-15 | 23-Jul-15 | 1 |
| L03-8632 | Install restroom accessories at Pool | 2 | 2 | 23-Jul-15 | 24-Jul-15 | 0 |
| L03-8646 | Health inspection | 1 | 1 | 27-Jul-15 | 27-Jul-15 | 0 |
| L03-8676 | Contractor Punchlist at Pool (inspect/distribute/correct | 3 | 3 | 28-Jul-15 | 30-Jul-15 | 0 |
| L03-8680 | Final Cleaning at Pool | 2 | 2 | 29-Jul-15 | 30-Jul-15 | 0 |
| L03-8678 | Owner Punchlist at Pool (inspect/distribute/correct) | 3 | 3 | 31-Jul-15 | 04-Aug-15 | 0 |
| CO-7168 | Final Inspections - Pool | 3 | 3 | 05-Aug-15 | 07-Aug-15 | 0 |
| CO-7008 | Substantial Completion - Pool | 0 | 0 | | 07-Aug-15 | 0 |
| **Milestones / Executive Summary / Misc** | | | | | | |
| **Contract Milestones** | | | | | | |
| CM-1000 | CM - Preliminary Permits / Design | 0 | 0 | 03-Aug-12 A | | |
| CM-1004 | CM - Notice to Proceed | 0 | 0 | 06-Mar-13 A | | |
| CM-1002 | CM - Contract Time (578 Cal Days) | 576 | 0 | 06-Mar-13 A | 05-Oct-14 A | |

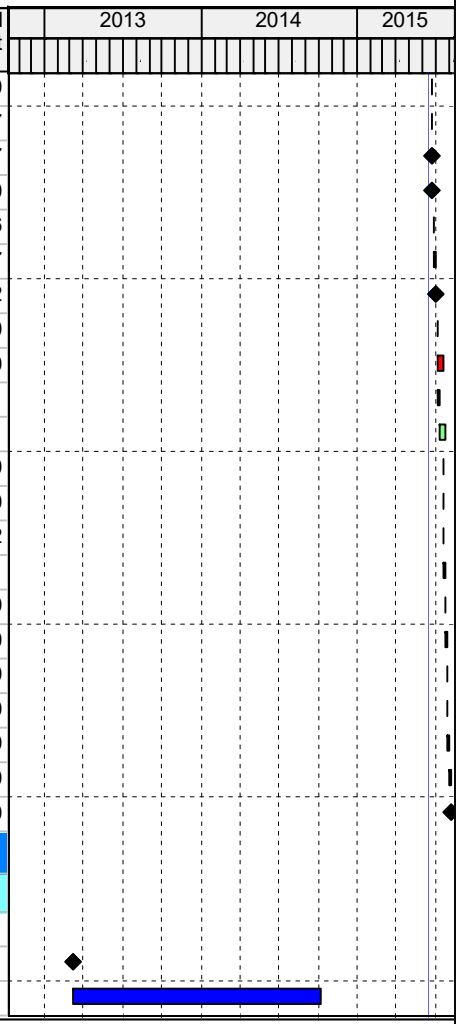


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| CM-1014 | CM - Start of Construction | 0 | 0 | 05-Apr-13 A | | |
| CM-1012 | CM - Begin Owner FF& E | 0 | 0 | 09-Mar-15 A | | |
| CM-1016 | CM - Owner FF+E "Build-Out" - Floors 4 & 5 | 7 | 0 | 09-Mar-15 A | 15-Mar-15 A | |
| CO-7004 | CO - Prep / Submit O&M Manuals [DELETED] | 14 | 0 | 01-May-15 A | 01-May-15 A | |
| CM-1006 | Construction Documents Issued by Client - (Due on 7 | 0 | 0 | 15-Jun-15 | | 22 |
| CM-1008 | Finalization of Allowances - (Due on 9-2-13) | 0 | 0 | 15-Jun-15 | | 22 |
| CM-1018 | CM - Hotel Operations Training | 14 | 14 | 18-Jun-15 | 01-Jul-15 | 37 |
| CO-7122 | TCO - Temporary Certificate of Occupancy | 0 | 0 | | 25-Jun-15 | 0 |
| CO-7006 | Substantial Completion - Podium & Tower | 0 | 0 | | 01-Jul-15* | 5 |
| **Misc Milestones** | | | | | | |
| CM-1020 | MM - Site Mobilization | 10 | 0 | 06-Mar-13 A | 04-Apr-13 A | |
| MM-1008 | MM - Top Out - Tower / Structure | 0 | 0 | | 16-Apr-14 A | |
| MM-1004 | MM - Start Drywall In Tower | 0 | 0 | 27-Jun-14 A | | |
| RF-4004 | MM - Tower Roof - Dry In | 0 | 0 | | 06-Sep-14 A | |
| MM-1010 | Energize Permanent Power | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| **Tower Crane / Man & Material Lifts** | | | | | | |
| **Tower Crane** | | | | | | |
| TC-5900 | Tower Crane - FRP Footings / Foundation | 5 | 0 | 04-Jun-13 A | 14-Jun-13 A | |
| TC-5904 | Tower Crane - Load Test / Certify | 1 | 0 | 20-Jun-13 A | 24-Jun-13 A | |
| TC-5902 | Tower Crane - Erectiion | 2 | 0 | 21-Jun-13 A | 24-Jun-13 A | |
| TC-5910 | Tower Crane - Erected / Certified | 0 | 0 | 24-Jun-13 A | | |
| TC-5906 | Tower Crane - Operatational Period | 391 | 0 | 24-Jun-13 A | 16-Jun-14 A | |
| TC-5908 | Tower Crane - Dismantle / Remove | 1 | 0 | 16-Jun-14 A | 17-Jun-14 A | |
| **Man & Material Lifts** | | | | | | |
| ML-5950 | Man/Material Lifts - FRP Footings / Foundation | 5 | 0 | 14-Jan-14 A | 20-Jan-14 A | |
| ML-5952 | Man/Material Lifts - Erect/Build Loading Dock | 5 | 0 | 21-Jan-14 A | 27-Jan-14 A | |
| ML-5956 | Man/Material Lifts - Certification | 0 | 0 | 10-Feb-14 A | | |

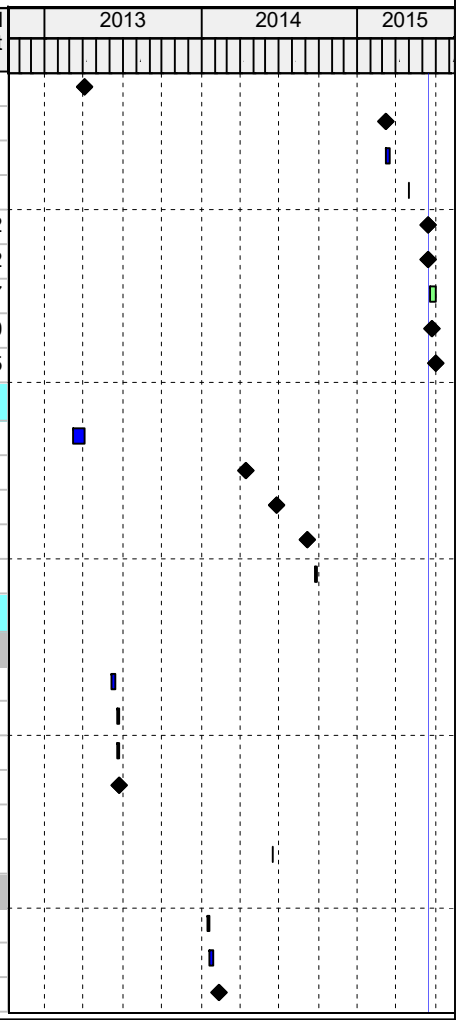


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| ML-5954 | Man/Material Lifts - Load Test / Certify | 1 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| ML-5958 | Man/Material Lifts - Operatational Period | 196 | 0 | 10-Feb-14 A | 15-Nov-14 A | |
| ML-5960 | Man/Material Lifts - Dismantle / Remove | 2 | 0 | 15-Nov-14 A | 16-Nov-14 A | |
| **Construction** | | | | | | |
| **Site Work / Excavation** | | | | | | |
| **Mass Excavation / Shoring** | | | | | | |
| SW-2000 | Erosion & Sedimentation Controls (SWPPP) | 3 | 0 | 05-Apr-13 A | 12-Apr-13 A | |
| SW-2002 | Demolition And Utility Relocation | 8 | 0 | 15-Apr-13 A | 19-Apr-13 A | |
| SW-2010 | Grade Subgrade for Elect/Plumbing | 3 | 0 | 07-Jan-14 A | 09-Jan-14 A | |
| **Site Finishes** | | | | | | |
| SW-2006 | Install Perm Power Electrical Service / Dry Utilities (Offl | 15 | 0 | 20-May-14 A | 05-Jun-14 A | |
| SW-2004 | Offsite Water & Water Connection | 9 | 0 | 22-Sep-14 A | 01-Oct-14 A | |
| SW-2008 | Zone 4 - Landscaping & irrigation | 15 | 0 | 13-Apr-15 A | 27-Apr-15 A | |
| **Structure** | | | | | | |
| **Foundation / Substructure - (Levels LL4 / LL3)** | | | | | | |
| **Lower Level 4 - (Parking / Mech Room)** | | | | | | |
| LL4-1602 | LL4 - FRP Matt Foundation / Footings | 15 | 0 | 12-Jun-13 A | 27-Jun-13 A | |
| LL4-1601 | LL4 - Excavate Footings | 14 | 0 | 17-Jun-13 A | 30-Jul-13 A | |
| LL4-1604 | LL4 - FRP Elevator Pit | 5 | 0 | 18-Jun-13 A | 24-Jun-13 A | |
| LL4-1606 | LL4 - Undrgmd Plumbing | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-1608 | LL4 - Undrgmd Elec | 5 | 0 | 18-Jun-13 A | 06-Aug-13 A | |
| LL4-2000 | LL4 - FRP Core Walls | 5 | 0 | 19-Jun-13 A | 25-Jun-13 A | |
| LL4-2002 | LL4 - FRP Columns / Misc Walls | 10 | 0 | 26-Jun-13 A | 02-Aug-13 A | |
| LL4-2033 | LL4 - Shotcrete Walls | 27 | 0 | 26-Jun-13 A | 05-Aug-13 A | |
| LL4-1620 | LL4 - Waterproof Walls | 3 | 0 | 03-Jul-13 A | 21-Aug-13 A | |
| LL4-1614 | LL4 - FRP SOG | 5 | 0 | 10-Jul-13 A | 07-Aug-13 A | |

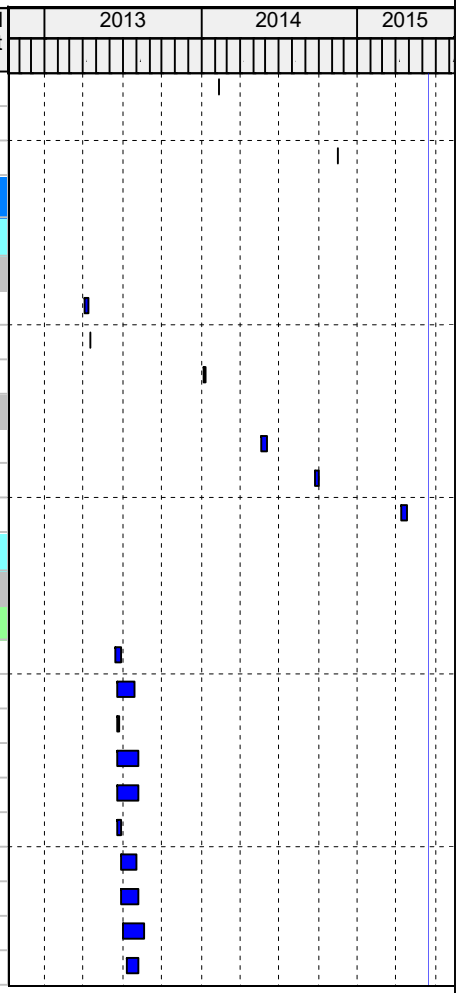



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL4-1610 | LL4 - FRP Ramp Walls | 5 | 0 | 12-Jul-13 A | 26-Jul-13 A | |
| LL4-1612 | LL4 - Cap Fill / Fine Grade | 3 | 0 | 13-Jul-13 A | 06-Aug-13 A | |
| LL4-1616 | LL4 - Backfill @ Ramp / Prep SOG | 2 | 0 | 22-Jul-13 A | 24-Jul-13 A | |
| LL4-1618 | LL4 - FRP Ramp SOG | 5 | 0 | 01-Aug-13 A | 07-Aug-13 A | |
| **Lower Level 3 - (Parking / Mech Room)** | | | | | | |
| LL3-2004 | LL2 - Shore / Form Deck | 8 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2006 | LL3 - M & E Inserts | 4 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2008 | LL3 - ReSteel / PT Cables | 6 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2010 | LL3 - Install Embeds | 2 | 0 | 05-Aug-13 A | 09-Aug-13 A | |
| LL3-2001 | LL3 - Waterproof Walls | 3 | 0 | 05-Aug-13 A | 05-Aug-13 A | |
| LL3-2012 | LL3 - Pour / Finish Deck | 2 | 0 | 16-Aug-13 A | 16-Aug-13 A | |
| LL3-2014 | LL3 - Stress Tendons | 1 | 0 | 19-Aug-13 A | 19-Aug-13 A | |
| LL3-2000 | LL3 - FRP Core Walls | 8 | 0 | 19-Aug-13 A | 28-Aug-13 A | |
| LL3-2033 | LL3 - Shotcrete Walls | 5 | 0 | 23-Aug-13 A | 26-Aug-13 A | |
| LL3-2016 | LL3 - Strip / ReShore Deck | 3 | 0 | 01-Sep-13 A | 13-Sep-13 A | |
| LL3-2018 | LL3 - Remove ReShores | 4 | 0 | 04-Nov-13 A | 07-Nov-13 A | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Grids 1 to 4 - (SOG @ Loading Dock)** | | | | | | |
| LL2-2056 | LL2 - Grease Intercepter | 5 | 0 | 15-Aug-13 A | 21-Aug-13 A | |
| LL2-2033 | LL2 - Shotcrete Walls | 6 | 0 | 27-Aug-13 A | 04-Sep-13 A | |
| LL2-2027 | LL2 - Waterproof Walls | 2 | 0 | 27-Aug-13 A | 28-Aug-13 A | |
| LL2-2007 | LL2 - FRP Elevator Pit @ Loading Dock | 4 | 0 | 30-Aug-13 A | 05-Sep-13 A | |
| LL2-2021 | LL2 - FRP Elec Vault | 14 | 0 | 30-Aug-13 A | 04-Sep-13 A | |
| LL2-2003 | LL2 - FRP 40k Fire Water Tank Ftgs / Walls | 5 | 0 | 04-Sep-13 A | 11-Sep-13 A | |
| LL2-2025 | LL2 - Waterproof Tanks | 2 | 0 | 11-Sep-13 A | 13-Sep-13 A | |
| LL2-2009 | LL2 - FRP 40k Water Tank Lid | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |

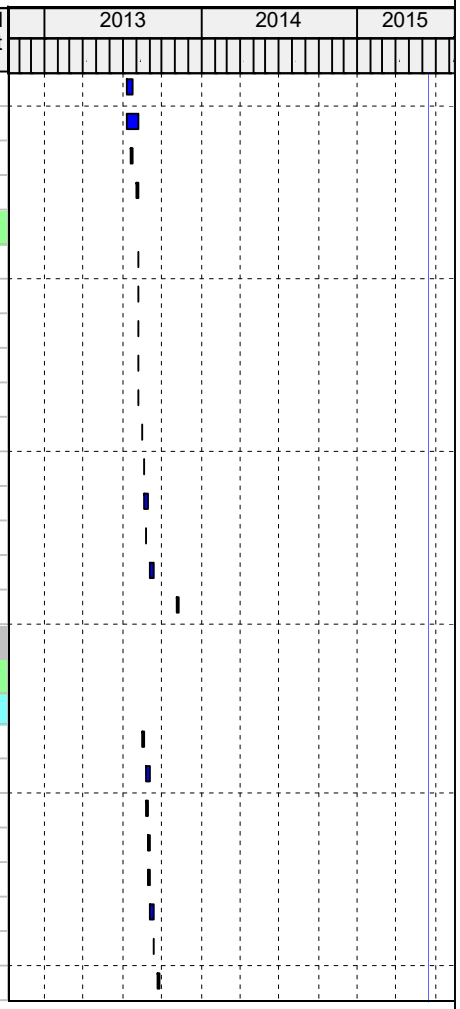



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL2-2005 | LL2 - FRP Detention Tank Ftgs / Walls/Roof | 11 | 0 | 19-Sep-13 A | 03-Oct-13 A | |
| LL2-2020 | LL2 - Undrgrnd Plumbing | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2022 | LL2 - Undrgrnd Elec | 10 | 0 | 19-Sep-13 A | 02-Oct-13 A | |
| LL2-2031 | LL2 - FRP Generator SOG | 3 | 0 | 19-Sep-13 A | 23-Sep-13 A | |
| LL2-2015 | LL2 to LL1 FRP Columns / Misc Walls | 6 | 0 | 01-Oct-13 A | 01-Oct-13 A | |
| LL2-2029 | LL2 - F/R/P Pour #2 | 8 | 0 | 15-Jan-14 A | 24-Jan-14 A | |
| LL2-2011 | LL2 - F/R/P Pour #3 | 16 | 0 | 24-Jan-14 A | 18-Feb-14 A | |
| LL2-2019 | LL2 - F/R/P Pour #6 | 4 | 0 | 19-Feb-14 A | 17-Mar-14 A | |
| LL2-2044 | LL2 - Set Generator | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| **Grids 10 to 24 - (PT Deck @ Parking / Laundry / Elec Rms)** | | | | | | |
| LL2-2004 | LL2 - Shore / Form Deck | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2035 | LL2 to LL1 - Shotcrete Walls | 8 | 0 | 12-Aug-13 A | 21-Aug-13 A | |
| LL2-2006 | LL2 - M & E Inserts | 4 | 0 | 14-Aug-13 A | 19-Aug-13 A | |
| LL2-2008 | LL2 - ReSteel / PT Cables | 6 | 0 | 14-Aug-13 A | 21-Aug-13 A | |
| LL2-2010 | LL2 - Install Embeds | 3 | 0 | 14-Aug-13 A | 16-Aug-13 A | |
| LL2-2002 | LL2 - FRP Columns / Misc Walls | 8 | 0 | 27-Aug-13 A | 06-Sep-13 A | |
| LL2-2012 | LL2 - Place / Finish Deck | 3 | 0 | 29-Aug-13 A | 29-Aug-13 A | |
| LL2-2023 | LL2 - Waterproof Walls | 3 | 0 | 29-Aug-13 A | 03-Sep-13 A | |
| LL2-2014 | LL2 - Stress Tendons | 1 | 0 | 30-Aug-13 A | 30-Aug-13 A | |
| LL2-2016 | LL2 - Strip / ReShore | 3 | 0 | 03-Sep-13 A | 05-Sep-13 A | |
| LL2-8234 | LL2 - Place / Finish Deck | 3 | 0 | 12-Sep-13 A | 12-Sep-13 A | |
| LL2-2000 | LL2 - FRP Core Walls | 8 | 0 | 12-Sep-13 A | 23-Sep-13 A | |
| LL2-2018 | LL2 - Remove ReShores | 4 | 0 | 13-Nov-13 A | 18-Nov-13 A | |
| LL2-2013 | LL2 - F/R/P Pour #1 | 4 | 0 | 13-Jan-14 A | 16-Jan-14 A | |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| P5A-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P5A-2000 | LL1 - FRP Core Walls | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |

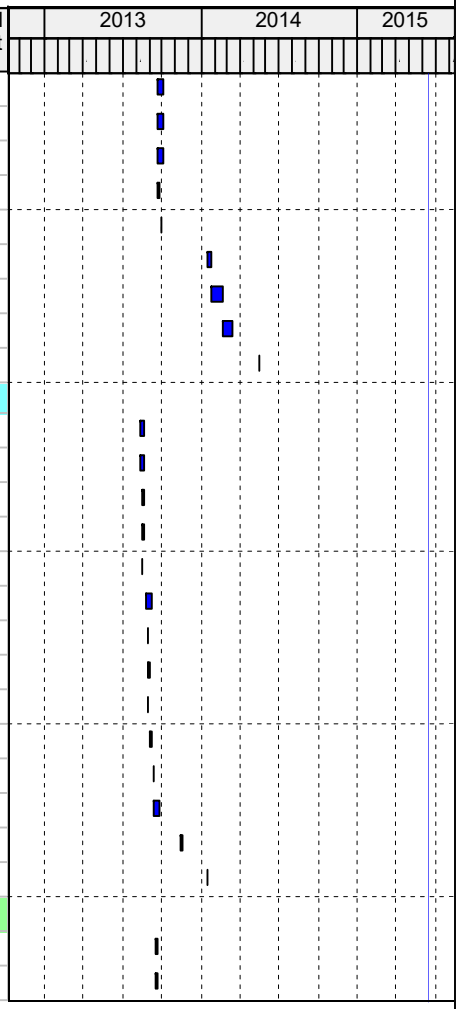


Actual Work | Critical Remai...
Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P5A-2004 | LL1 - Shore / Form Deck | 3 | 0 | 16-Sep-13 A | 18-Sep-13 A | |
| P6-2002 | LL1 - FRP Columns Below | 5 | 0 | 16-Sep-13 A | 20-Sep-13 A | |
| P6-2004 | LL1 - Shore / Form Deck | 7 | 0 | 16-Sep-13 A | 24-Sep-13 A | |
| P5A-2006 | LL1 - MEP Rough In | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2008 | LL1 - ReSteel / PT Cables | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 18-Sep-13 A | 19-Sep-13 A | |
| P5A-2012 | LL1 - Place / Finish Deck | 0 | 0 | 20-Sep-13 A | | |
| P5A-2020 | LL1 - Waterproof Walls | 3 | 0 | 20-Sep-13 A | 24-Sep-13 A | |
| P5A-2014 | LL1 - Stress Tendons | 1 | 0 | 23-Sep-13 A | 23-Sep-13 A | |
| P5A-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2006 | LL1 - MEP Rough In | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2008 | LL1 - ReSteel / PT Cables | 3 | 0 | 24-Sep-13 A | 26-Sep-13 A | |
| P6-2010 | LL1 - Install Edgeform/Embeds | 2 | 0 | 24-Sep-13 A | 25-Sep-13 A | |
| P6-2020 | LL1 - Waterproof Walls | 4 | 0 | 24-Sep-13 A | 27-Sep-13 A | |
| P5A-2033 | LL1 - Resteel/Shotcrete Walls | 3 | 0 | 25-Sep-13 A | 27-Sep-13 A | |
| P5B-2002 | LL1 - FRP Columns Below | 5 | 0 | 26-Sep-13 A | 02-Oct-13 A | |
| P5B-2004 | LL1 - Shore / Form Deck | 7 | 0 | 26-Sep-13 A | 04-Oct-13 A | |
| P6-2012 | LL1 - Place / Finish Deck | 0 | 0 | 27-Sep-13 A | | |
| P6-2014 | LL1 - Stress Tendons | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2033 | LL1 - Resteel/Shotcrete Walls | 1 | 0 | 30-Sep-13 A | 30-Sep-13 A | |
| P6-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 01-Oct-13 A | 03-Oct-13 A | |
| P5B-2006 | LL1 - MEP Rough In | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2002 | FRP Columns Below | 5 | 0 | 03-Oct-13 A | 09-Oct-13 A | |
| P10A--2004 | Shore / Form Deck | 4 | 0 | 03-Oct-13 A | 08-Oct-13 A | |
| P5B-2008 | LL1 - ReSteel / PT Cables | 5 | 0 | 04-Oct-13 A | 10-Oct-13 A | |
| P5B-2010 | LL1 - Install Edgeform/Embeds | 4 | 0 | 04-Oct-13 A | 09-Oct-13 A | |
| P8-2002 | FRP Columns Below | 5 | 0 | 07-Oct-13 A | 11-Oct-13 A | |

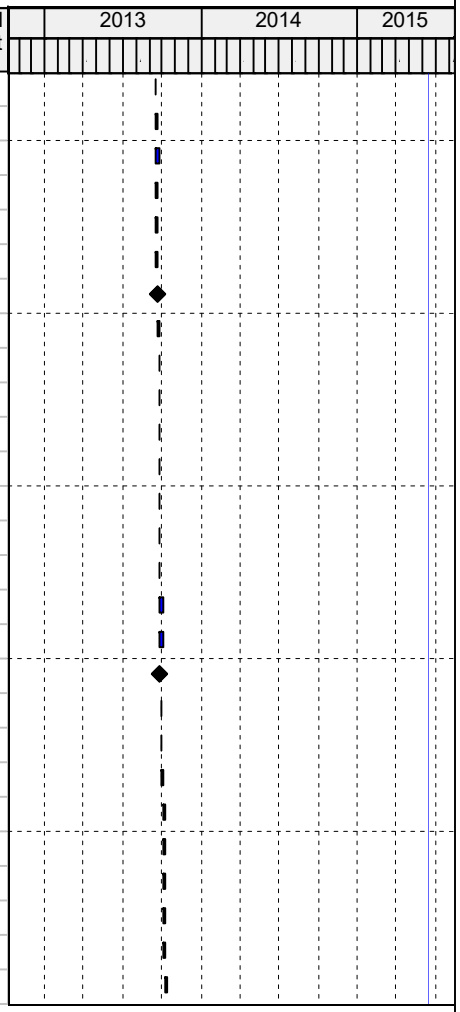


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P8-2000 | Form/Resteel/Close Core Walls | 14 | 0 | 07-Oct-13 A | 24-Oct-13 A | |
| P8-2004 | Shore / Form Deck P8 | 8 | 0 | 07-Oct-13 A | 16-Oct-13 A | |
| P7-2002 | FRP Columns Below | 5 | 0 | 08-Oct-13 A | 14-Oct-13 A | |
| P7-2004 | Shore / Form Deck | 6 | 0 | 08-Oct-13 A | 15-Oct-13 A | |
| P10A--2006 | MEP Rough In | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2008 | ReSteel / PT Cables | 3 | 0 | 08-Oct-13 A | 10-Oct-13 A | |
| P10A--2010 | Install Edgeform/Embeds | 2 | 0 | 08-Oct-13 A | 09-Oct-13 A | |
| P5B-2012 | LL1 - Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P10A--2012 | Place / Finish Deck | 0 | 0 | 11-Oct-13 A | | |
| P5B-2014 | LL1 - Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P7-2006 | MEP Rough In | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P7-2008 | ReSteel / PT Cables | 4 | 0 | 14-Oct-13 A | 17-Oct-13 A | |
| P10A--2014 | Stress Tendons | 1 | 0 | 14-Oct-13 A | 14-Oct-13 A | |
| P8-2020 | Shore / Form Deck P9 | 6 | 0 | 14-Oct-13 A | 21-Oct-13 A | |
| P5B-2016 | LL1 - Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2010 | Install Edgeform/Embeds | 2 | 0 | 15-Oct-13 A | 16-Oct-13 A | |
| P8-2006 | MEP Rough In | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2008 | ReSteel / PT Cables | 8 | 0 | 15-Oct-13 A | 24-Oct-13 A | |
| P8-2010 | Install Edgeform/Embeds | 4 | 0 | 15-Oct-13 A | 18-Oct-13 A | |
| P10A--2016 | Strip / ReShore Deck | 3 | 0 | 15-Oct-13 A | 17-Oct-13 A | |
| P7-2012 | Place / Finish Deck | 0 | 0 | 18-Oct-13 A | | |
| P7-2033 | Resteel/Shotcrete Walls | 3 | 0 | 18-Oct-13 A | 22-Oct-13 A | |
| P7-2014 | Stress Tendons | 1 | 0 | 21-Oct-13 A | 21-Oct-13 A | |
| P7-2016 | Strip / ReShore Deck | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2002 | FRP Columns Below | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |
| P10B--2000 | FRP Shear Walls Below | 3 | 0 | 22-Oct-13 A | 24-Oct-13 A | |
| P10B--2004 | Shore / Form Deck | 5 | 0 | 22-Oct-13 A | 28-Oct-13 A | |

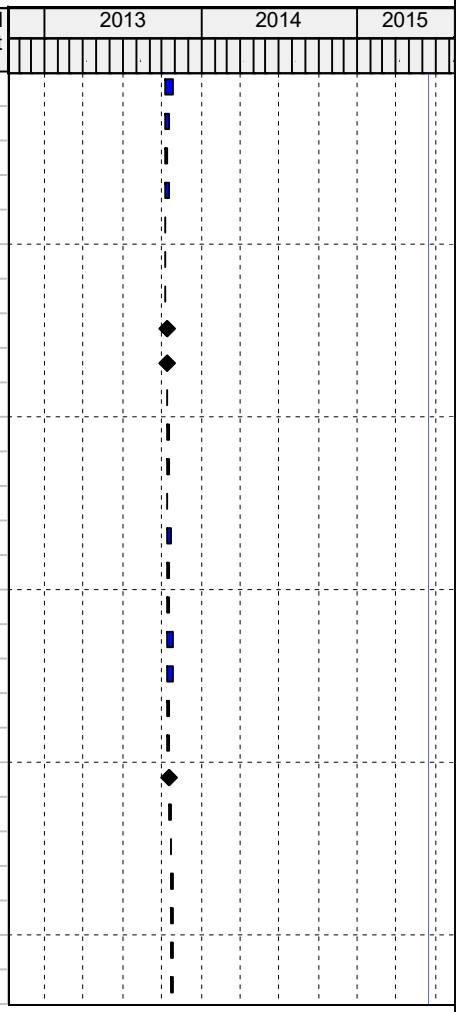


Actual Work | Critical Remai... | Remaining Work | Milestone | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P8-2012 | Place / Finish Deck P 8 & 9 and Core Walls | 0 | 0 | 25-Oct-13 A | | |
| P8-2014 | Stress Tendons | 1 | 0 | 28-Oct-13 A | 28-Oct-13 A | |
| P10B--2006 | MEP Rough In | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2008 | ReSteel / PT Cables | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P10B--2010 | Install Edgeform/Embeds | 3 | 0 | 28-Oct-13 A | 30-Oct-13 A | |
| P12--2002 | FRP Columns Below | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P12--2000 | Form/Resteel/Close Core Walls | 9 | 0 | 28-Oct-13 A | 07-Nov-13 A | |
| P12--2004 | Shore / Form Deck | 5 | 0 | 28-Oct-13 A | 01-Nov-13 A | |
| P8-2016 | Strip / ReShore Deck | 3 | 0 | 29-Oct-13 A | 31-Oct-13 A | |
| P11--2002 | FRP Columns Below | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P11--2004 | Shore / Form Deck | 5 | 0 | 29-Oct-13 A | 04-Nov-13 A | |
| P10B--2012 | Place / Finish Deck | 0 | 0 | 31-Oct-13 A | | |
| P10B--2014 | Stress Tendons | 1 | 0 | 01-Nov-13 A | 01-Nov-13 A | |
| P12--2006 | MEP Rough In | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12--2008 | ReSteel / PT Cables | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P12--2010 | Install Edgeform/Embeds | 3 | 0 | 01-Nov-13 A | 05-Nov-13 A | |
| P10B--2016 | Strip / ReShore Deck | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2006 | MEP Rough In | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2008 | ReSteel / PT Cables | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2010 | Install Edgeform/Embeds | 3 | 0 | 04-Nov-13 A | 06-Nov-13 A | |
| P11--2012 | Place / Finish Deck | 0 | 0 | 07-Nov-13 A | | |
| P13--2002 | FRP Columns Below | 5 | 0 | 07-Nov-13 A | 14-Nov-13 A | |
| P13--2004 | Shore / Form Deck | 9 | 0 | 07-Nov-13 A | 28-Nov-13 A | |
| P11--2014 | Stress Tendons | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| P12--2012 | Place / Finish Deck & Core Walls | 0 | 0 | 08-Nov-13 A | | |
| P11--2016 | Strip / ReShore Deck | 3 | 0 | 12-Nov-13 A | 14-Nov-13 A | |
| P12--2014 | Stress Tendons | 1 | 0 | 12-Nov-13 A | 12-Nov-13 A | |

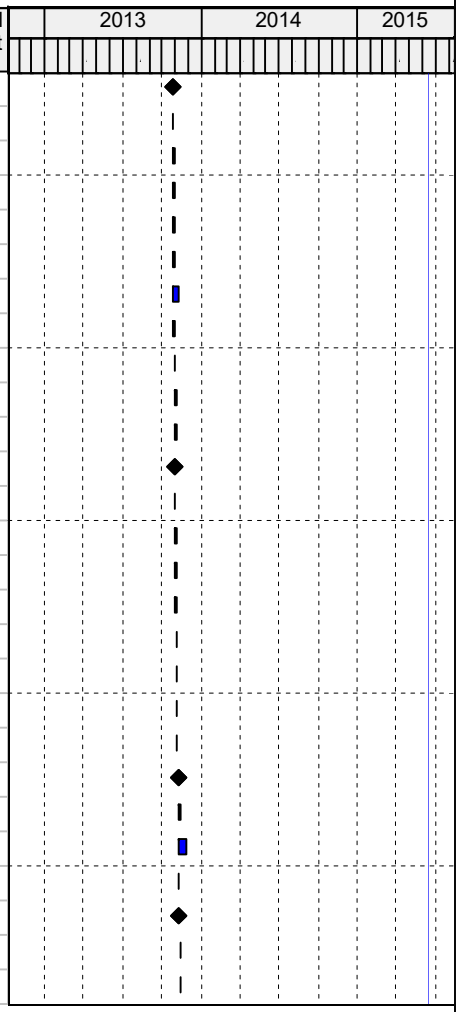



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P14–2002 | FRP Columns Below | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P14–2000 | Form/Resteel/Close Core Walls | 8 | 0 | 19-Nov-13 A | 03-Dec-13 A | |
| P14–2004 | Shore / Form Deck | 5 | 0 | 19-Nov-13 A | 25-Nov-13 A | |
| P13A–2002 | FRP Columns Below | 5 | 0 | 21-Nov-13 A | 27-Nov-13 A | |
| P13A–2004 | Shore / Form Deck | 4 | 0 | 21-Nov-13 A | 26-Nov-13 A | |
| P13–2010 | Install Edgeform/Embeds | 5 | 0 | 22-Nov-13 A | 04-Dec-13 A | |
| P13–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2006 | MEP Rough In | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2008 | ReSteel / PT Cables | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P14–2010 | Install Edgeform/Embeds | 5 | 0 | 25-Nov-13 A | 03-Dec-13 A | |
| P13–2006 | MEP Rough In | 5 | 0 | 26-Nov-13 A | 03-Dec-13 A | |
| P13A–2006 | MEP Rough In | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2008 | ReSteel / PT Cables | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13A–2010 | Install Edgeform/Embeds | 3 | 0 | 26-Nov-13 A | 02-Dec-13 A | |
| P13–2012 | Place / Finish Deck | 0 | 0 | 02-Dec-13 A | | |
| P13A–2012 | Place / Finish Deck | 0 | 0 | 03-Dec-13 A | | |
| P14–2012 | Place / Finish Deck & Core Walls | 0 | 0 | 04-Dec-13 A | | |
| P13–2014 | Stress Tendons | 1 | 0 | 05-Dec-13 A | 05-Dec-13 A | |
| P15–2002 | FRP Columns Below | 3 | 0 | 05-Dec-13 A | 09-Dec-13 A | |
| P15–2000 | Jump/Resteel/Close Core | 9 | 0 | 05-Dec-13 A | 17-Dec-13 A | |
| P15–2004 | Shore / Form Deck | 5 | 0 | 05-Dec-13 A | 11-Dec-13 A | |
| P13–2016 | Strip / ReShore Deck | 3 | 0 | 06-Dec-13 A | 10-Dec-13 A | |
| P13A–2014 | Stress Tendons | 1 | 0 | 06-Dec-13 A | 06-Dec-13 A | |
| P14–2014 | Stress Tendons | 1 | 0 | 07-Dec-13 A | 07-Dec-13 A | |
| P15–2006 | MEP Rough In | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2008 | ReSteel / PT Cables | 5 | 0 | 11-Dec-13 A | 17-Dec-13 A | |
| P15–2010 | Install Edgeform/Embeds | 3 | 0 | 11-Dec-13 A | 13-Dec-13 A | |

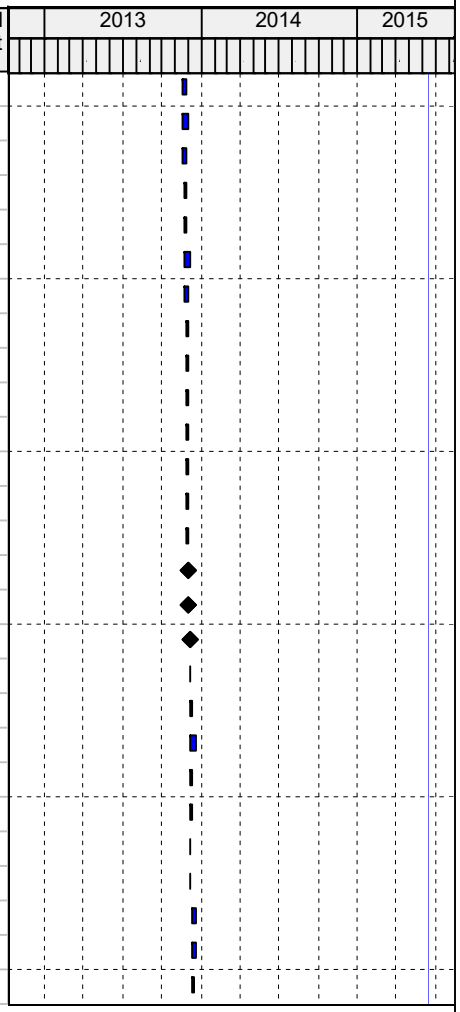



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P16-2002 | FRP Columns Below | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P16-2004 | Shore / Form Deck | 5 | 0 | 16-Dec-13 A | 20-Dec-13 A | |
| P15--2012 | Place / Finish Deck | 0 | 0 | 18-Dec-13 A | | |
| P15--2020 | Place Conc @ Core | 0 | 0 | 18-Dec-13 A | | |
| P16-2000 | Jump/Resteel/Close Core | 5 | 0 | 18-Dec-13 A | 24-Dec-13 A | |
| P16-2006 | MEP Rough In | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2008 | ReSteel / PT Cables | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P16-2010 | Install Edgeform/Embeds | 3 | 0 | 20-Dec-13 A | 24-Dec-13 A | |
| P15--2014 | Stress Tendons | 1 | 0 | 21-Dec-13 A | 21-Dec-13 A | |
| P8-2018 | Remove Reshores | 2 | 0 | 23-Dec-13 A | 24-Dec-13 A | |
| P10A--2018 | Remove Reshores | 2 | 0 | 26-Dec-13 A | 27-Dec-13 A | |
| P16-2012 | Place / Finish Deck | 0 | 0 | 26-Dec-13 A | | |
| P16-2020 | Place Conc @ Core | 0 | 0 | 26-Dec-13 A | | |
| P17-2002 | FRP Columns Below | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P17-2000 | Jump/Resteel/Close Core | 7 | 0 | 27-Dec-13 A | 07-Jan-14 A | |
| P17-2004 | Shore / Form Deck | 5 | 0 | 27-Dec-13 A | 03-Jan-14 A | |
| P10B--2018 | Remove Reshores | 2 | 0 | 30-Dec-13 A | 31-Dec-13 A | |
| P16-2014 | Stress Tendons | 1 | 0 | 31-Dec-13 A | 31-Dec-13 A | |
| P5A-2018 | LL1 - Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P11--2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P12--2018 | Remove Reshores | 2 | 0 | 02-Jan-14 A | 03-Jan-14 A | |
| P17-2006 | MEP Rough In | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2008 | ReSteel / PT Cables | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P17-2010 | Install Edgeform/Embeds | 3 | 0 | 03-Jan-14 A | 07-Jan-14 A | |
| P6-2018 | LL1 - Remove Reshores | 2 | 0 | 06-Jan-14 A | 07-Jan-14 A | |
| P5B-2018 | LL1 - Remove Reshores | 2 | 0 | 08-Jan-14 A | 09-Jan-14 A | |
| P17-2012 | Place / Finish Deck | 0 | 0 | 08-Jan-14 A | | |

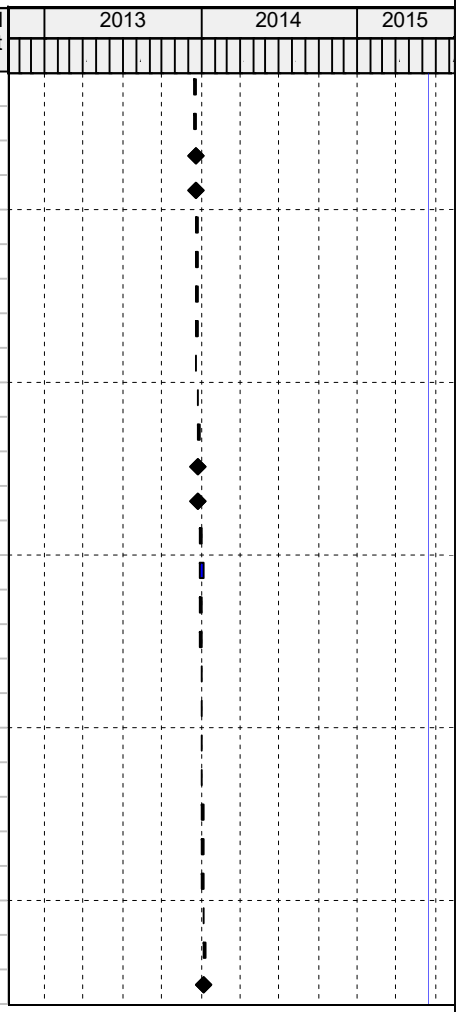



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P17-2020 | Place Conc @ Core | 0 | 0 | 08-Jan-14 A | | |
| P18-2002 | FRP Columns Below | 5 | 0 | 09-Jan-14 A | 15-Jan-14 A | |
| P18-2000 | Jump/Resteel/Close Core | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P18-2004 | Shore / Form Deck | 3 | 0 | 09-Jan-14 A | 13-Jan-14 A | |
| LL2-2022R | MEP Rough In | 4 | 0 | 09-Jan-14 A | 14-Jan-14 A | |
| P7-2018 | Remove Reshores | 2 | 0 | 10-Jan-14 A | 13-Jan-14 A | |
| P17-2014 | Stress Tendons | 1 | 0 | 11-Jan-14 A | 11-Jan-14 A | |
| P13–2018 | Remove Reshores | 2 | 0 | 13-Jan-14 A | 14-Jan-14 A | |
| P13A–2018 | Remove Reshores | 2 | 0 | 15-Jan-14 A | 16-Jan-14 A | |
| WEA-2012 | WIND IMPACT | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| P18-2006 | MEP Rough In | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2008 | ReSteel / PT Cables | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2010 | Install Edgeform/Embeds | 2 | 0 | 20-Jan-14 A | 21-Jan-14 A | |
| P18-2012 | Place / Finish Deck | 0 | 0 | 22-Jan-14 A | | |
| P18-2020 | Place Conc @ Core | 0 | 0 | 22-Jan-14 A | | |
| P19-2002 | FRP Columns Below | 5 | 0 | 23-Jan-14 A | 29-Jan-14 A | |
| P19-2000 | Jump/Resteel/Close Core | 4 | 0 | 23-Jan-14 A | 28-Jan-14 A | |
| P19-2004 | Shore / Form Deck | 3 | 0 | 23-Jan-14 A | 27-Jan-14 A | |
| P18-2014 | Stress Tendons | 1 | 0 | 25-Jan-14 A | 25-Jan-14 A | |
| P14–2018 | Remove Reshores | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2006 | MEP Rough In | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2008 | ReSteel / PT Cables | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2010 | Install Edgeform/Embeds | 2 | 0 | 27-Jan-14 A | 28-Jan-14 A | |
| P19-2012 | Place / Finish Deck | 0 | 0 | 29-Jan-14 A | | |
| P19-2020 | Place Conc @ Core | 0 | 0 | 29-Jan-14 A | | |
| P20-2002 | FRP Columns Below | 5 | 0 | 30-Jan-14 A | 05-Feb-14 A | |
| P20-2000 | Jump/Resteel/Close Core | 9 | 0 | 30-Jan-14 A | 11-Feb-14 A | |

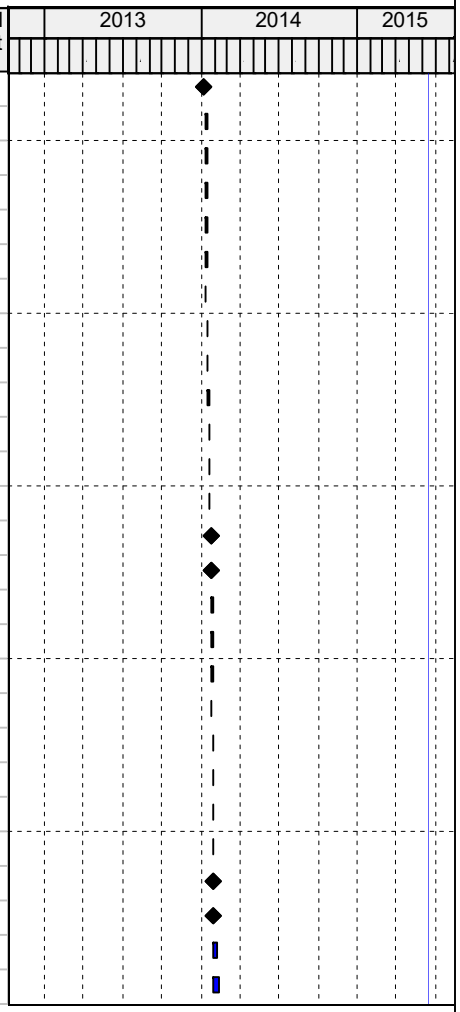



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P20-2004 | Shore / Form Deck | 6 | 0 | 30-Jan-14 A | 10-Feb-14 A | |
| P19-2014 | Stress Tendons | 1 | 0 | 01-Feb-14 A | 01-Feb-14 A | |
| P13A–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P14–2016 | Strip / ReShore Deck | 3 | 0 | 05-Feb-14 A | 07-Feb-14 A | |
| P15–2016 | Strip / ReShore Deck | 3 | 0 | 06-Feb-14 A | 10-Feb-14 A | |
| P20-2006 | MEP Rough In | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2008 | ReSteel / PT Cables | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| P20-2010 | Install Edgeform/Embeds | 4 | 0 | 06-Feb-14 A | 11-Feb-14 A | |
| L03-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 06-Feb-14 A | 12-Feb-14 A | |
| P16-2016 | Strip / ReShore Deck | 3 | 0 | 10-Feb-14 A | 12-Feb-14 A | |
| L04-2018 | Remove Reshores | 2 | 0 | 10-Feb-14 A | 11-Feb-14 A | |
| L03-2018 | Remove Reshores | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| P17-2016 | Strip / ReShore Deck | 3 | 0 | 12-Feb-14 A | 14-Feb-14 A | |
| P20-2012 | Place / Finish Deck | 0 | 0 | 12-Feb-14 A | | |
| P20-2020 | Place Conc @ Core | 0 | 0 | 12-Feb-14 A | | |
| L04-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-Feb-14 A | 18-Feb-14 A | |
| P12–2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P18-2016 | Strip / ReShore Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P21-2002 | FRP Columns Below | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| P21-2000 | Jump/Resteel/Close Core | 4 | 0 | 13-Feb-14 A | 18-Feb-14 A | |
| P21-2004 | Shore / Form Deck | 3 | 0 | 13-Feb-14 A | 17-Feb-14 A | |
| P19-2016 | Strip / ReShore Deck | 3 | 0 | 14-Feb-14 A | 18-Feb-14 A | |
| P20-2014 | Stress Tendons | 1 | 0 | 15-Feb-14 A | 15-Feb-14 A | |
| P21-2006 | MEP Rough In | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2008 | ReSteel / PT Cables | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P21-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| P20-2016 | Strip / ReShore Deck | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |

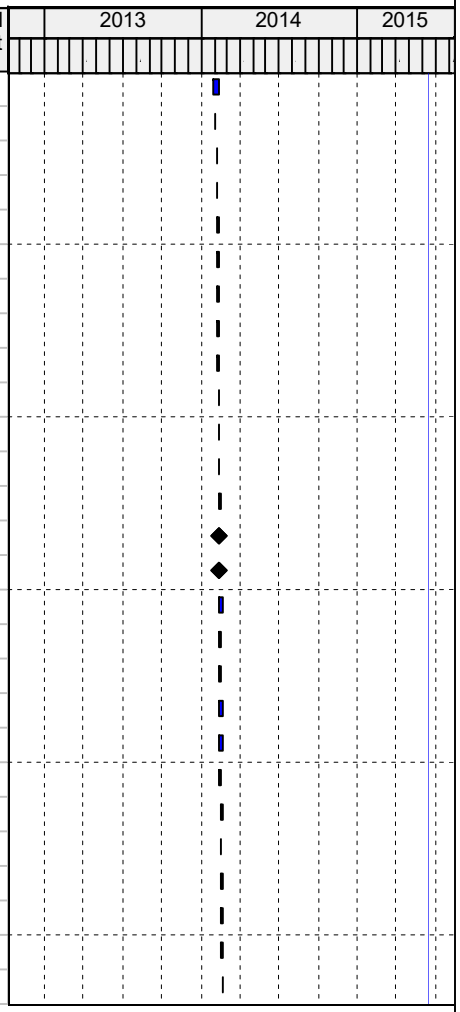



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-2018 | Remove Reshores | 2 | 0 | 18-Feb-14 A | 19-Feb-14 A | |
| P21-2012 | Place / Finish Deck | 0 | 0 | 19-Feb-14 A | | |
| P21-2020 | Place Conc @ Core | 0 | 0 | 19-Feb-14 A | | |
| P22-2002 | FRP Columns Below | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P22-2000 | Jump/Resteel/Close Core | 4 | 0 | 20-Feb-14 A | 25-Feb-14 A | |
| P22-2004 | Shore / Form Deck | 3 | 0 | 20-Feb-14 A | 24-Feb-14 A | |
| L05-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 20-Feb-14 A | 26-Feb-14 A | |
| P21-2014 | Stress Tendons | 1 | 0 | 22-Feb-14 A | 22-Feb-14 A | |
| P21-2016 | Strip / ReShore Deck | 3 | 0 | 24-Feb-14 A | 26-Feb-14 A | |
| P22-2006 | MEP Rough In | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2008 | ReSteel / PT Cables | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| P22-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| L06-2018 | Remove Reshores | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| P22-2012 | Place / Finish Deck | 0 | 0 | 26-Feb-14 A | | |
| P22-2020 | Place Conc @ Core | 0 | 0 | 26-Feb-14 A | | |
| P23-2002 | FRP Columns Below | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2000 | Jump/Resteel/Close Core | 4 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2004 | Shore / Form Deck | 3 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| P23-2006 | MEP Rough In | 2 | 0 | 01-Mar-14 A | 03-Mar-14 A | |
| P22-2014 | Stress Tendons | 1 | 0 | 01-Mar-14 A | 01-Mar-14 A | |
| P23-2008 | ReSteel / PT Cables | 2 | 0 | 03-Mar-14 A | 04-Mar-14 A | |
| P22-2016 | Strip / ReShore Deck | 3 | 0 | 04-Mar-14 A | 10-Mar-14 A | |
| P23-2010 | Install Edgeform/Embeds | 2 | 0 | 04-Mar-14 A | 04-Mar-14 A | |
| L07-2018 | Remove Reshores | 2 | 0 | 04-Mar-14 A | 05-Mar-14 A | |
| P23-2012 | Place / Finish Deck | 0 | 0 | 05-Mar-14 A | | |
| P23-2020 | Place Conc @ Core | 0 | 0 | 05-Mar-14 A | | |
| P24-2002 | FRP Columns Below | 5 | 0 | 05-Mar-14 A | 07-Mar-14 A | |

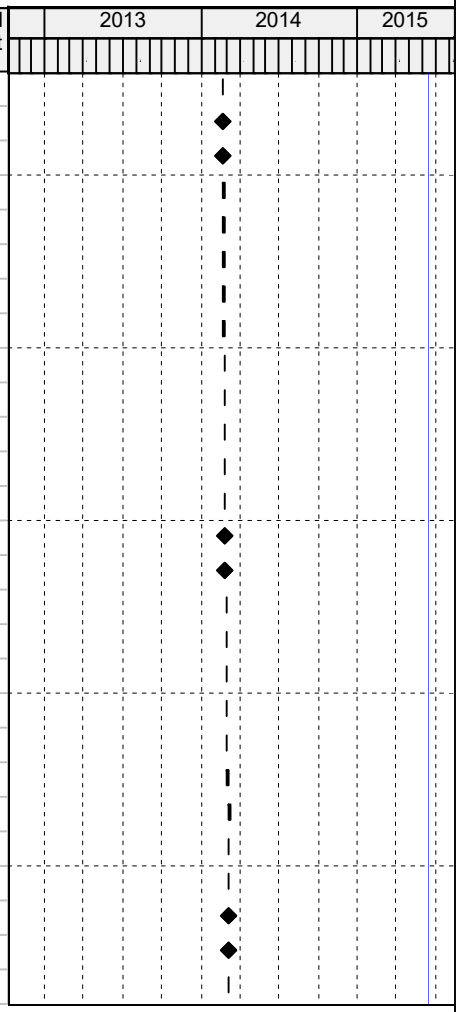



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P24-2004 | Shore / Form Deck | 3 | 0 | 06-Mar-14 A | 10-Mar-14 A | |
| P24-2000 | Jump/Resteel/Close Core | 4 | 0 | 08-Mar-14 A | 10-Mar-14 A | |
| P23-2014 | Stress Tendons | 1 | 0 | 10-Mar-14 A | 10-Mar-14 A | |
| P24-2008 | ReSteel / PT Cables | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P24-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Mar-14 A | 11-Mar-14 A | |
| P23-2016 | Strip / ReShore Deck | 3 | 0 | 11-Mar-14 A | 17-Mar-14 A | |
| P24-2006 | MEP Rough In | 2 | 0 | 11-Mar-14 A | 11-Mar-14 A | |
| P25-2002 | FRP Columns Below | 5 | 0 | 11-Mar-14 A | 13-Mar-14 A | |
| L08-2018 | Remove Reshores | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| P24-2012 | Place / Finish Deck | 0 | 0 | 12-Mar-14 A | | |
| P24-2020 | Place Conc @ Core | 0 | 0 | 12-Mar-14 A | | |
| P25-2004 | Shore / Form Deck | 3 | 0 | 13-Mar-14 A | 17-Mar-14 A | |
| P25-2000 | Jump/Resteel/Close Core | 4 | 0 | 15-Mar-14 A | 17-Mar-14 A | |
| P24-2014 | Stress Tendons | 1 | 0 | 17-Mar-14 A | 17-Mar-14 A | |
| P25-2006 | MEP Rough In | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2008 | ReSteel / PT Cables | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| P25-2010 | Install Edgeform/Embeds | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| L06-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 18-Mar-14 A | 20-Mar-14 A | |
| L09-2018 | Remove Reshores | 2 | 0 | 18-Mar-14 A | 19-Mar-14 A | |
| P26-2002 | FRP Columns Below | 5 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| P25-2012 | Place / Finish Deck | 0 | 0 | 19-Mar-14 A | | |
| P25-2020 | Place Conc @ Core | 0 | 0 | 19-Mar-14 A | | |
| P26-2004 | Shore / Form Deck | 3 | 0 | 20-Mar-14 A | 24-Mar-14 A | |
| L07-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 21-Mar-14 A | 25-Mar-14 A | |
| P26-2000 | Jump/Resteel/Close Core | 4 | 0 | 22-Mar-14 A | 24-Mar-14 A | |
| P26-2006 | MEP Rough In | 2 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P26-2008 | ReSteel / PT Cables | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |

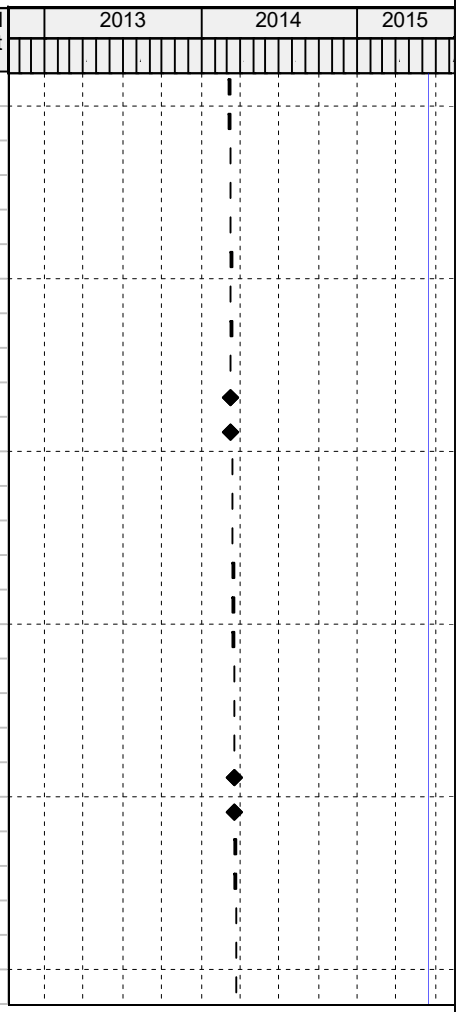



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P26-2010 | Install Edgeform/Embeds | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| P25-2014 | Stress Tendons | 1 | 0 | 24-Mar-14 A | 24-Mar-14 A | |
| P27-2002 | FRP Columns Below | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| P26-2012 | Place / Finish Deck | 0 | 0 | 26-Mar-14 A | | |
| P26-2020 | Place Conc @ Core | 0 | 0 | 26-Mar-14 A | | |
| L08-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 26-Mar-14 A | 28-Mar-14 A | |
| L10-2018 | Remove Reshores | 2 | 0 | 26-Mar-14 A | 27-Mar-14 A | |
| P27-2004 | Shore / Form Deck | 3 | 0 | 27-Mar-14 A | 31-Mar-14 A | |
| P27-2000 | Jump/Resteel/Close Core | 4 | 0 | 29-Mar-14 A | 31-Mar-14 A | |
| P27-2006 | MEP Rough In | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2008 | ReSteel / PT Cables | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P27-2010 | Install Edgeform/Embeds | 2 | 0 | 31-Mar-14 A | 01-Apr-14 A | |
| P26-2014 | Stress Tendons | 1 | 0 | 31-Mar-14 A | 31-Mar-14 A | |
| L09-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 31-Mar-14 A | 02-Apr-14 A | |
| P24-2016 | Strip / ReShore Deck | 3 | 0 | 01-Apr-14 A | 07-Apr-14 A | |
| L11-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 02-Apr-14 A | |
| L12-2018 | Remove Reshores | 2 | 0 | 01-Apr-14 A | 03-Apr-14 A | |
| P27-2012 | Place / Finish Deck | 0 | 0 | 02-Apr-14 A | | |
| P27-2020 | Place Conc @ Core | 0 | 0 | 02-Apr-14 A | | |
| P28-2002 | FRP Columns Below | 5 | 0 | 02-Apr-14 A | 04-Apr-14 A | |
| P28-2004 | Shore / Form Deck | 4 | 0 | 03-Apr-14 A | 08-Apr-14 A | |
| L10-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| P27-2014 | Stress Tendons | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| P25-2016 | Strip / ReShore Deck | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L14-2018 | Remove Reshores | 2 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| P28-2000 | Jump/Resteel/Close Core | 7 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| P28-2006 | MEP Rough In | 4 | 0 | 08-Apr-14 A | 10-Apr-14 A | |

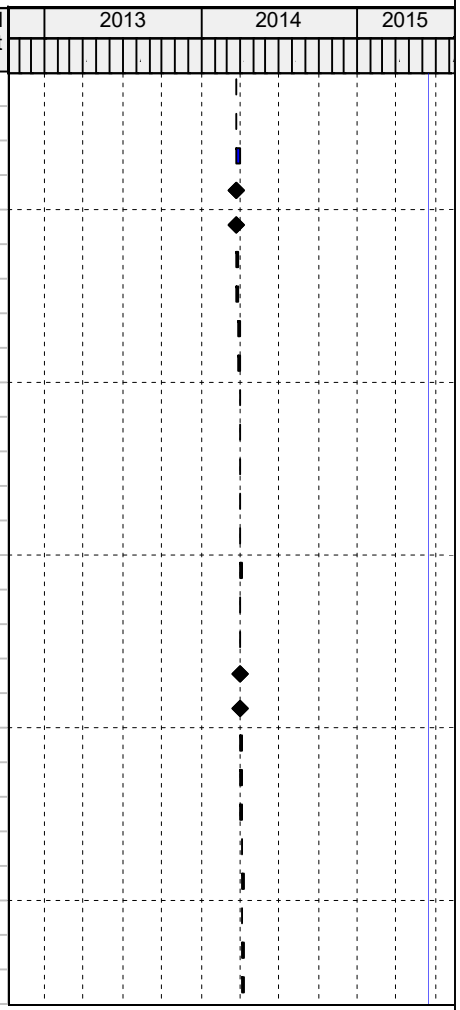



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| P28-2008 | ReSteel / PT Cables | 4 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 08-Apr-14 A | 10-Apr-14 A | |
| P28-2010 | Install Edgeform/Embeds | 2 | 0 | 10-Apr-14 A | 11-Apr-14 A | |
| L12-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| P28-2012 | Place / Finish Deck | 0 | 0 | 14-Apr-14 A | | |
| P28-2020 | Place Conc @ Core | 0 | 0 | 14-Apr-14 A | | |
| P29-2002 | FRP Columns Above Roof Deck | 3 | 0 | 14-Apr-14 A | 18-Apr-14 A | |
| P26-2016 | Strip / ReShore Deck | 3 | 0 | 14-Apr-14 A | 17-Apr-14 A | |
| L14-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-Apr-14 A | 18-Apr-14 A | |
| P28-2014 | Stress Tendons | 1 | 0 | 17-Apr-14 A | 17-Apr-14 A | |
| P29-2000 | Strip Core | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| P27-2016 | Strip / ReShore Deck | 3 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L15-2018 | Remove Reshores | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| P28-2016 | Strip / ReShore Deck | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L15-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L16-2019 | Grind Ceiling for Skim Coat | 5 | 0 | 16-May-14 A | 19-May-14 A | |
| L16-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2018 | Remove Reshores | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L17-2019 | Grind Ceiling for Skim Coat | 2 | 0 | 23-Jun-14 A | 24-Jun-14 A | |
| **Ballroom Catwalk & Roof** | | | | | | |
| PC-2100 | Erect Structural Steel @ Porte Cochere | 3 | 0 | 30-Jan-14 A | 03-Feb-14 A | |
| BR-2100 | BR - Erect Structural Steel / Girders @ Ballroom Catw | 7 | 0 | 07-Feb-14 A | 17-Feb-14 A | |
| BR-2102 | BR - Metal Decking @ Ballroom Catwalk / Roof | 3 | 0 | 18-Feb-14 A | 20-Feb-14 A | |
| PC-2102 | Metal Decking @ Porte Cochere/ Roof | 2 | 0 | 17-Apr-14 A | 18-Apr-14 A | |
| BR-2112 | BR - Fireproofing @ Structural Steel | 2 | 0 | 27-May-14 A | 30-May-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Mech Penthouse** | | | | | | |

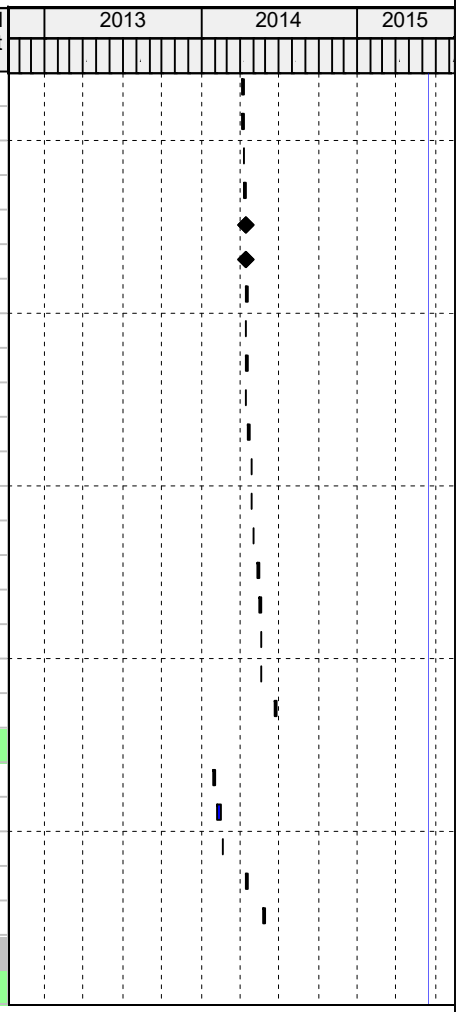



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-8706 | Set Mech Equipment @ Tower Roof | 3 | 0 | 22-May-14 A | 28-May-14 A | |
| PH-8708 | Set Equipment @ Penthouse | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| PH-8700 | PH - Structural Steel and Decking | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| **Vertical Circulation** | | | | | | |
| Stairs | | | | | | |
| **Stair 1 - (Core Tower) - LL4 to PH** | | | | | | |
| S1-4000 | Stair 1 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 25-Nov-13 A | 26-Nov-13 A | |
| S1-4002 | Stair 1 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 27-Nov-13 A | 03-Dec-13 A | |
| S1-4004 | Stair 1 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 04-Dec-13 A | 05-Dec-13 A | |
| S1-4006 | Stair 1 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 06-Dec-13 A | 09-Dec-13 A | |
| S1-4008 | Stair 1 - Set Mtl Stairs / Railings L1 | 2 | 0 | 03-Feb-14 A | 04-Feb-14 A | |
| S1-4016 | Stair 1 - Set Mtl Stairs / Railings L5 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4010 | Stair 1 - Set Mtl Stairs / Railings L2 | 2 | 0 | 05-Feb-14 A | 06-Feb-14 A | |
| S1-4018 | Stair 1 - Set Mtl Stairs / Railings L6 | 2 | 0 | 06-Feb-14 A | 07-Feb-14 A | |
| S1-4020 | Stair 1 - Set Mtl Stairs / Railings L7 | 2 | 0 | 07-Feb-14 A | 07-Feb-14 A | |
| S1-4012 | Stair 1 - Set Mtl Stairs / Railings L3 | 2 | 0 | 07-Feb-14 A | 10-Feb-14 A | |
| S1-4022 | Stair 1 - Set Mtl Stairs / Railings L8 | 2 | 0 | 10-Feb-14 A | 10-Feb-14 A | |
| S1-4014 | Stair 1 - Set Mtl Stairs / Railings L4 | 2 | 0 | 11-Feb-14 A | 12-Feb-14 A | |
| S1-4024 | Stair 1 - Set Mtl Stairs / Railings L9 | 2 | 0 | 06-Mar-14 A | 07-Mar-14 A | |
| S1-4026 | Stair 1 - Set Mtl Stairs / Railings L10 | 2 | 0 | 07-Mar-14 A | 10-Mar-14 A | |
| S1-4028 | Stair 1 - Set Mtl Stairs / Railings L11 | 2 | 0 | 11-Mar-14 A | 12-Mar-14 A | |
| S1-4030 | Stair 1 - Set Mtl Stairs / Railings L12 | 2 | 0 | 13-Mar-14 A | 14-Mar-14 A | |
| S1-4032 | Stair 1 - Set Mtl Stairs / Railings L14 | 2 | 0 | 08-Apr-14 A | 21-Apr-14 A | |
| S1-4034 | Stair 1 - Set Mtl Stairs / Railings L15 | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| S1-4036 | Stair 1 - Set Mtl Stairs / Railings L16 | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| S1-4038 | Stair 1 - Set Mtl Stairs / Railings L17 | 2 | 0 | 27-May-14 A | 28-May-14 A | |
| S1-4040 | Stair 1 - Set Mtl Stairs / Railings L18 | 2 | 0 | 27-May-14 A | 28-May-14 A | |

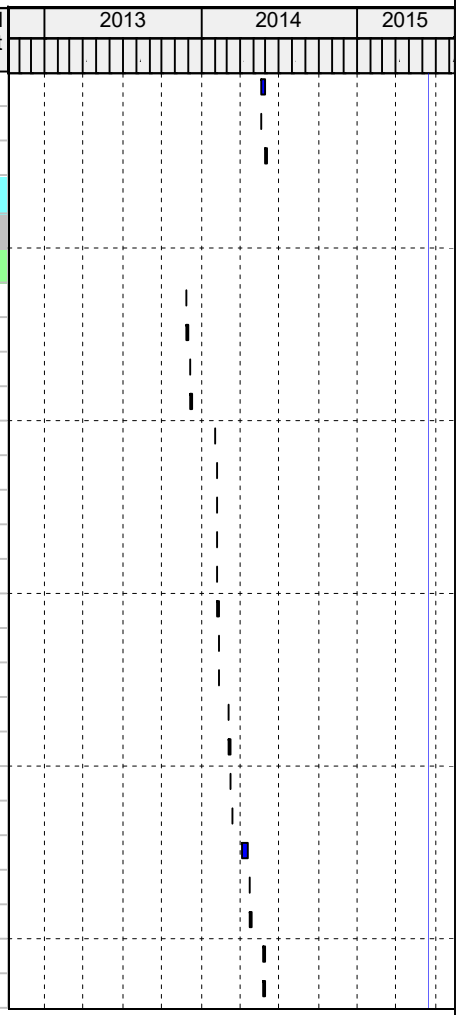



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Stair 2 - (South Tower) - LL4 to 17** | | | | | | |
| S2-4000 | Stair 2 - Set Mtl Stairs / Railings LL4 | 2 | 0 | 10-Dec-13 A | 11-Dec-13 A | |
| S2-4002 | Stair 2 - Set Mtl Stairs / Railings LL3 | 2 | 0 | 12-Dec-13 A | 13-Dec-13 A | |
| S2-4004 | Stair 2 - Set Mtl Stairs / Railings LL2 | 2 | 0 | 16-Dec-13 A | 17-Dec-13 A | |
| S2-4006 | Stair 2 - Set Mtl Stairs / Railings LL1 | 2 | 0 | 18-Dec-13 A | 19-Dec-13 A | |
| S2-4016 | Stair 2 - Set Mtl Stairs / Railings L5 | 2 | 0 | 12-Feb-14 A | 13-Feb-14 A | |
| S2-4018 | Stair 2 - Set Mtl Stairs / Railings L6 | 2 | 0 | 13-Feb-14 A | 13-Feb-14 A | |
| S2-4008 | Stair 2 - Set Mtl Stairs / Railings L1 | 2 | 0 | 13-Feb-14 A | 14-Feb-14 A | |
| S2-4010 | Stair 2 - Set Mtl Stairs / Railings L2 | 2 | 0 | 17-Feb-14 A | 18-Feb-14 A | |
| S2-4012 | Stair 2 - Set Mtl Stairs / Railings L3 | 2 | 0 | 19-Feb-14 A | 20-Feb-14 A | |
| S2-4014 | Stair 2 - Set Mtl Stairs / Railings L4 | 2 | 0 | 21-Feb-14 A | 24-Feb-14 A | |
| S2-4020 | Stair 2 - Set Mtl Stairs / Railings L7 | 2 | 0 | 24-Feb-14 A | 25-Feb-14 A | |
| S2-4022 | Stair 2 - Set Mtl Stairs / Railings L8 | 2 | 0 | 25-Feb-14 A | 26-Feb-14 A | |
| S2-4024 | Stair 2 - Set Mtl Stairs / Railings L9 | 2 | 0 | 17-Mar-14 A | 18-Mar-14 A | |
| S2-4026 | Stair 2 - Set Mtl Stairs / Railings L10 | 2 | 0 | 19-Mar-14 A | 20-Mar-14 A | |
| S2-4028 | Stair 2 - Set Mtl Stairs / Railings L11 | 2 | 0 | 21-Mar-14 A | 22-Mar-14 A | |
| S2-4030 | Stair 2 - Set Mtl Stairs / Railings L12 | 2 | 0 | 24-Mar-14 A | 25-Mar-14 A | |
| S2-4032 | Stair 2 - Set Mtl Stairs / Railings L14 | 2 | 0 | 21-Apr-14 A | 22-Apr-14 A | |
| S2-4034 | Stair 2 - Set Mtl Stairs / Railings L15 | 2 | 0 | 14-May-14 A | 15-May-14 A | |
| S2-4036 | Stair 2 - Set Mtl Stairs / Railings L16 | 2 | 0 | 16-May-14 A | 19-May-14 A | |
| S2-4038 | Stair 2 - Set Mtl Stairs / Railings L17 | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| **Stair 3 - (Southeast Podium) - LL2 to 1** | | | | | | |
| S3-4000 | Stair 3 - Set Metal Stairs / Railings LL2 | 6 | 0 | 05-Mar-14 A | 20-Mar-14 A | |
| S3-4002 | Stair 3 - Set Metal Stairs / Railings LL1 | 6 | 0 | 17-Mar-14 A | 21-Mar-14 A | |
| S3-4004 | Stair 3 - Paint walls & railings | 4 | 0 | 04-May-15 A | 11-May-15 A | |
| **Stair 4 - (Northeast Podium) - LL2 to 2** | | | | | | |
| S4-4000 | Stair 4 - Set Metal Stairs / Railings LL2 | 6 | 0 | 15-May-14 A | 20-May-14 A | |

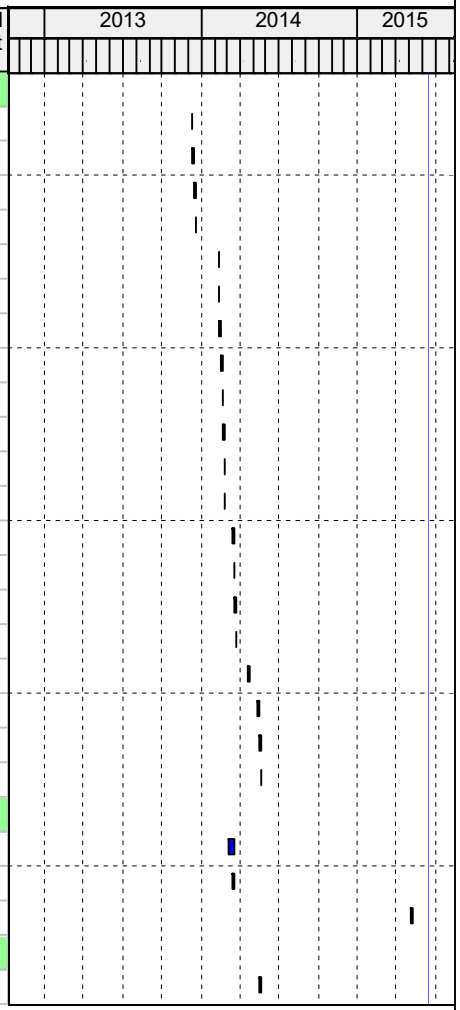



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| S4-4002 | Stair 4 - Set Metal Stairs / Railings LL1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4004 | Stair 4 -Set Metal Stairs / Railings L1 | 6 | 0 | 15-May-14 A | 20-May-14 A | |
| S4-4006 | Stair 4 - Paint walls & railings | 4 | 0 | 28-Apr-15 A | 01-May-15 A | |
| **Stair 6 - (North Exercise) LL1 to Exterior** | | | | | | |
| S6-4000 | Stair 6 - Set Metal Stairs / Railings | 5 | 0 | 25-Jun-14 A | 01-Jul-14 A | |
| S6-4002 | Stair 6 - Paint walls & railings | 2 | 0 | 01-Apr-15 A | 03-Apr-15 A | |
| **Stair 7 - (Generator) LL2** | | | | | | |
| S7-4000 | Stair 7 - Mtl Stairs / Railings @ Generator Rm | 4 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| **Stair 5 - (Grand Staircase) - LL1 to 1** | | | | | | |
| GS-4000 | Grand Stairs - FRP Stairs | 10 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| GS-4002 | Grand Stairs - Permanent Railings / Final Finishes (DE | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| **Stair 4a - (Pool) - 3** | | | | | | |
| S4a-4000 | Stair 4a -Set Metal Stairs / Railings L1 | 5 | 0 | 01-Aug-14 A | 01-Aug-14 A | |
| S4a-4002 | Stair 4a - Paint walls & railings | 2 | 0 | 04-May-15 A | 08-May-15 A | |
| **Elevators** | | | | | | |
| EL-1000 | Elev - Recieve IFC Drawings & NTP | 0 | 0 | 07-Jun-13 A | | |
| EL-1002 | Elev - Design Submittal Preparation (Engineered Gea | 49 | 0 | 17-Jun-13 A | 21-Jun-13 A | |
| EL-1004 | Elev - Submittal Approval | 21 | 0 | 21-Jun-13 A | 01-Jan-14 A | |
| EL-1006 | Elev - Release to Manufacturing | 14 | 0 | 02-Jan-14 A | 15-Jan-14 A | |
| EL-1008 | Elev - Fabrication (Engineered Geared) | 95 | 0 | 16-Jan-14 A | 14-Jun-14 A | |
| EL-1010 | Elev - Machines delivered | 1 | 0 | 12-May-14 A | 12-May-14 A | |
| EL-1011 | Elev - Elevator Machines Flown & Set At Top Of Hoist | 5 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| **Service Elevator 5 - LL4 to PH - (21 Floors)** | | | | | | |
| EL-5016 | Elev 5 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-1216 | Elev 1&2 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-3416 | Elev 3&4 - Hoistway Walls Complete (GC) | 0 | 0 | | 01-Jan-14 A | |
| EL-5002 | Elev 5 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |

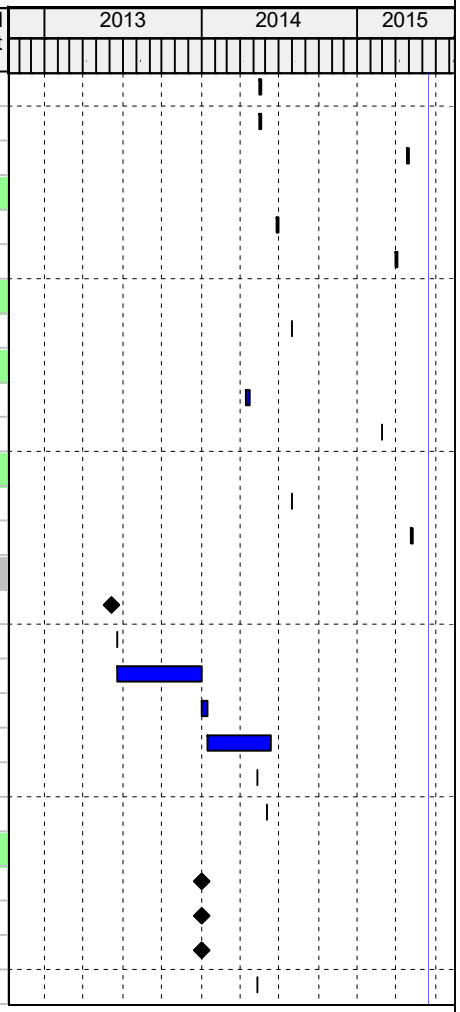



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-1202 | Elev 1&2 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-3402 | Elev 3&4 - Mob / Unload & Stage Equip / Materials | 2 | 0 | 12-May-14 A | 13-May-14 A | |
| EL-5018 | Elev 5 - Set Hoistway Machines | 3 | 0 | 02-Jun-14 A | 02-Jun-14 A | |
| EL-1218 | Elev 1&2 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-3418 | Elev 3&4 - Set Hoistway Machines | 3 | 0 | 03-Jun-14 A | 03-Jun-14 A | |
| EL-1200 | Elev 1&2 - Hoistway Clear & Ready (GC) | 0 | 0 | 20-Jun-14 A | | |
| EL-1204 | Elev 1&2 - Install Rails & Brackets | 17 | 0 | 23-Jun-14 A | 15-Jul-14 A | |
| EL-3400 | Elev 3&4 - Hoistway Clear & Ready (GC) | 0 | 0 | 23-Jun-14 A | | |
| EL-6000 | Elev 6 - Hoistway Clear & Ready (GC) | 0 | 0 | 24-Jun-14 A | | |
| EL-1206 | Elev 1&2 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Jul-14 A | |
| EL-1207 | Elev 1&2 - Install Pit Equipment/Car Sling/CWT Fram | 3 | 0 | 15-Jul-14 A | 01-Aug-14 A | |
| EL-1208 | Elev 1&2 - Install MHoist & Cable | 5 | 0 | 16-Jul-14 A | 24-Jul-14 A | |
| EL-3407 | Elev 3&4 - Install Pit Equipment/Car Sling/CWT Fram | 5 | 0 | 16-Jul-14 A | 06-Aug-14 A | |
| EL-5000 | Elev 5 - Hoistway Clear & Ready (GC) | 0 | 0 | 21-Jul-14 A | | |
| EL-5004 | Elev 5 - Install Rails & Brackets | 13 | 0 | 21-Jul-14 A | 11-Aug-14 A | |
| EL-3404 | Elev 3&4 - Install Rails & Brackets | 18 | 0 | 23-Jul-14 A | 04-Aug-14 A | |
| EL-3406 | Elev 3&4 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 28-Jul-14 A | |
| EL-3408 | Elev 3&4 - Install Hoist & Cable | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| EL-5007 | Elev 5 - Install Pit Equipment/Car Sling/CWT Frame/V | 5 | 0 | 12-Aug-14 A | 15-Aug-14 A | |
| EL-1210 | Elev 1&2 - Install Entrances/Doors/Fixtures/Fascia | 19 | 0 | 14-Aug-14 A | 22-Sep-14 A | |
| EL-3410 | Elev 3&4 - Install Entrances/Doors/Fixtures/Fascia | 30 | 0 | 14-Aug-14 A | 02-Oct-14 A | |
| EL-5006 | Elev 5 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 15-Aug-14 A | |
| EL-5008 | Elev 5 - Install MHoist & Cable | 4 | 0 | 18-Aug-14 A | 20-Aug-14 A | |
| EL-5010 | Elev 5 - Install Entrances/Doors/Fixtures/Fascia | 21 | 0 | 21-Aug-14 A | 26-Sep-14 A | |
| EL-1212 | Elev 1&2 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 22-Sep-14 A | 13-Oct-14 A | |
| EL-5012 | Elev 5 - Install Hoistway Equipment/Pipe & Wire | 14 | 0 | 26-Sep-14 A | 16-Oct-14 A | |
| EL-3412 | Elev 3&4 - Install Hoistway Equipment/Pipe & Wire | 23 | 0 | 03-Oct-14 A | 03-Nov-14 A | |

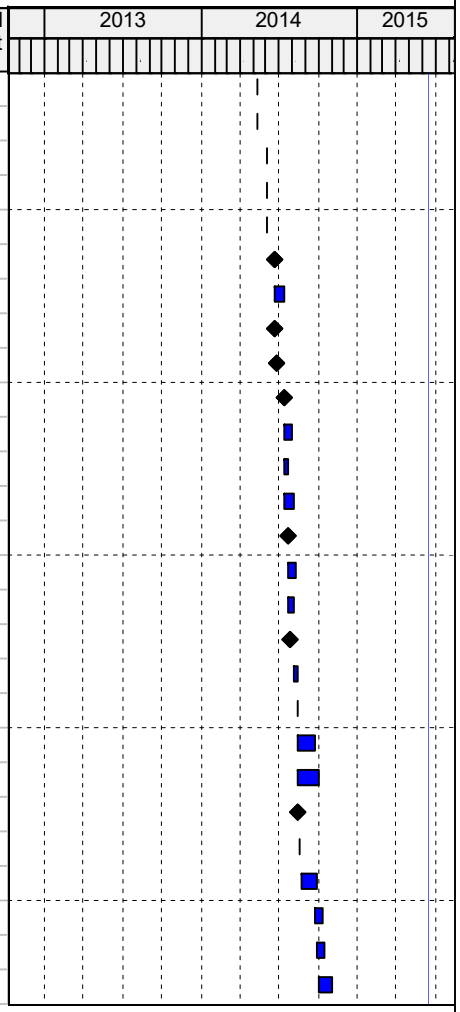



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| EL-1214 | Elev 1&2 - Install Cab/Wiring/Door Operator(s) | 11 | 0 | 14-Oct-14 A | 28-Oct-14 A | |
| EL-5014 | Elev 5 - Install Cab/Wiring/Door Operator(s) | 7 | 0 | 17-Oct-14 A | 27-Oct-14 A | |
| EL-6002 | Elev 6 - Mob / Unload & Stage Equip / Materials | 1 | 0 | 24-Oct-14 A | 24-Oct-14 A | |
| EL-6016 | Elev 6 - Hoistway Walls Complete (GC) | 0 | 0 | | 24-Oct-14 A | |
| EL-6004 | Elev 6 - Install Cylinders/Rails & Brackets | 4 | 0 | 27-Oct-14 A | 30-Oct-14 A | |
| EL-5022 | Elev 5 - Adjust | 5 | 0 | 28-Oct-14 A | 03-Nov-14 A | |
| EL-1222 | Elev 1&2 - Adjust | 5 | 0 | 29-Oct-14 A | 04-Nov-14 A | |
| EL-6006 | Elev 6 - Enclosed Mech Room With Power (GC) | 0 | 0 | | 30-Oct-14 A | |
| EL-6007 | Elev 6 - Install Pit Equipment/Car Sling | 2 | 0 | 31-Oct-14 A | 03-Nov-14 A | |
| EL-5024 | Elev 5 - Clean / Paint / Punchlist | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| EL-3414 | Elev 3&4 - Install Cab/Wiring/Door Operator(s) | 10 | 0 | 04-Nov-14 A | 17-Nov-14 A | |
| EL-6018 | Elev 6 - Install Machine Room Equipment | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| EL-1224 | Elev 1&2 - Clean / Paint / Punchlist | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| EL-5026 | Elev 5 - Inspections | 7 | 0 | 13-Nov-14 A | 14-Nov-14 A | |
| EL-3422 | Elev 3&4 - Adjust | 8 | 0 | 18-Nov-14 A | 20-Nov-14 A | |
| EL-6012 | Elev 6 - Install hoistway rails & divider beams | 2 | 0 | 20-Nov-14 A | 21-Nov-14 A | |
| EL-6010 | Elev 6 - Install elevator fronts/rears | 9 | 0 | 09-Dec-14 A | 24-Dec-14 A | |
| EL-6014 | Elev 6 - Cab build-out | 5 | 0 | 15-Dec-14 A | 30-Jan-15 A | |
| EL-6022 | Elev 6 - Final cleaning at EMR | 4 | 0 | 25-Feb-15 A | 27-Feb-15 A | |
| EL-1226 | Elev 1&2 - CoB/L&I Inspections (for FF&E use) | 3 | 0 | 04-Mar-15 A | 06-Mar-15 A | |
| EL-3424 | Elev 3&4 - Walsh/TKE pre-inspection | 6 | 0 | 27-Mar-15 A | 27-Mar-15 A | |
| EL-6024 | Elev 6 - Walsh/TKE pre-inspection | 2 | 0 | 13-Apr-15 A | 14-Apr-15 A | |
| EL-3426 | Elev 3&4 - CoB/L&I Inspections (Final) | 2 | 0 | 19-May-15 A | 20-May-15 A | |
| EL-6026 | Elev 6 - CoB/L&I Inspections (Final) | 2 | 0 | 19-May-15 A | 20-May-15 A | |
| **Exterior Shell** | | | | | | |
| **Elevations** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |

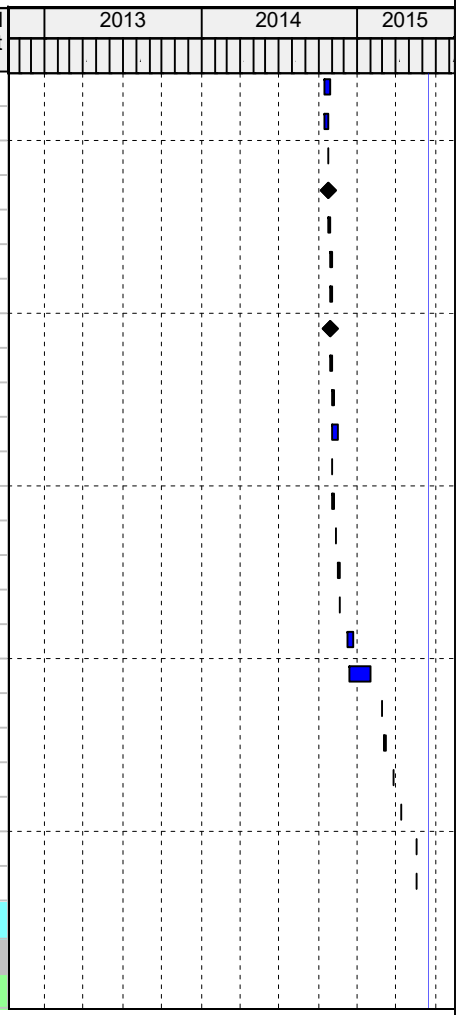



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Lower Level 2** | | | | | | |
| L3D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Feb-14 A | 12-Feb-14 A | |
| L3-5308 | L3- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 17-Feb-14 A | 21-Feb-14 A | |
| L4D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Feb-14 A | 19-Feb-14 A | |
| L4-5308 | L4- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Feb-14 A | 28-Feb-14 A | |
| L5D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Feb-14 A | 26-Feb-14 A | |
| L5-5308 | L5- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 03-Mar-14 A | 07-Mar-14 A | |
| L6D5308 | Deliver/Stock Wall Panels | 1 | 0 | 05-Mar-14 A | 05-Mar-14 A | |
| L6-5308 | L6- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L7-5308 | L7- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L7D5308 | Deliver/Stock Wall Panels | 1 | 0 | 12-Mar-14 A | 12-Mar-14 A | |
| L8D5308 | Deliver/Stock Wall Panels | 1 | 0 | 19-Mar-14 A | 19-Mar-14 A | |
| L8-5308 | L8- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Mar-14 A | 28-Mar-14 A | |
| L9D5308 | Deliver/Stock Wall Panels | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L9-5308 | L9- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 31-Mar-14 A | 07-Apr-14 A | |
| 10D5308 | Deliver/Stock Wall Panels | 1 | 0 | 02-Apr-14 A | 02-Apr-14 A | |
| L10-5308 | L10- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 07-Apr-14 A | 11-Apr-14 A | |
| 11D5308 | Deliver/Stock Wall Panels | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L11-5308 | L11- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 11-Apr-14 A | 18-Apr-14 A | |
| 12D5308 | Deliver/Stock Wall Panels | 1 | 0 | 16-Apr-14 A | 16-Apr-14 A | |
| L12-5308 | L12- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 21-Apr-14 A | 25-Apr-14 A | |
| 14D5308 | Deliver/Stock Wall Panels | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L14-5308 | L14 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 24-Apr-14 A | 01-May-14 A | |
| 15D5308 | Deliver/Stock Wall Panels | 1 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L15-5308 | L15 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| 16D5308 | Deliver/Stock Wall Panels | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L16-5308 | L16- Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 09-May-14 A | 14-May-14 A | |

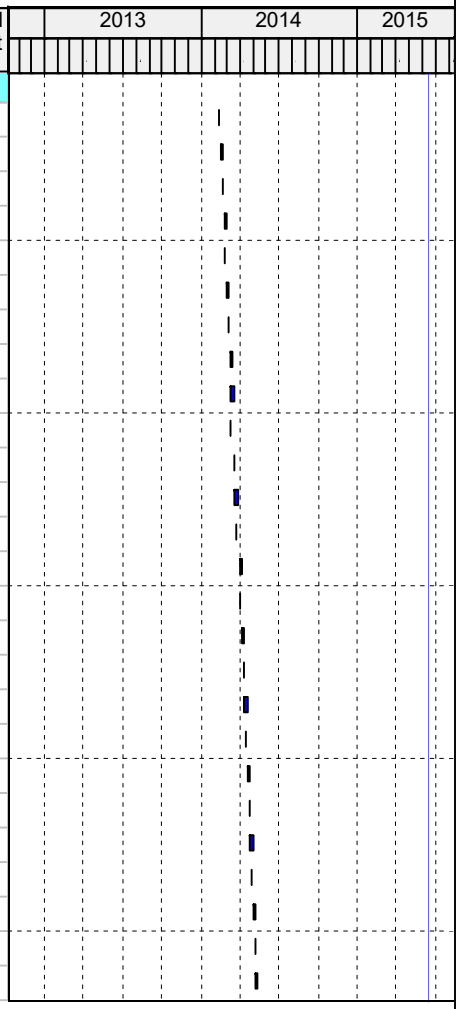


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| 17D5308 | Deliver/Stock Wall Panels | 1 | 0 | 14-May-14 A | 14-May-14 A | |
| L17-5308 | L17 - Support Frame/Sheathing for Metal Wall Panels | 5 | 0 | 20-May-14 A | 11-Jun-14 A | |
| LL2-5308 | LL2 Thru L4 - Support Frame/Sheathing for Metal Wa | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| LL1-5308 | LL1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| L1-5308 | L1 - Support Frame/Sheathing for Metal Wall Panels | 6 | 0 | 19-Jun-14 A | 06-Aug-14 A | |
| **Level 1** | | | | | | |
| L3-5102 | L3- Storefront Frames | 7 | 0 | 18-Aug-14 A | 29-Sep-14 A | |
| L1-5102 | L1 - Storefront Frames (excl. Main Entry Facade) | 8 | 0 | 02-Sep-14 A | 11-Sep-14 A | |
| L1-5104 | L1 - Storefront Glazing (excl. Main Entry Facade) | 4 | 0 | 19-Sep-14 A | 24-Sep-14 A | |
| EP-5110 | L1 - Revolving Doors | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| L3-5104 | L3 - Storefront Glazing | 3 | 0 | 30-Sep-14 A | 03-Oct-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Levels 3-4** | | | | | | |
| L3-5130 | L3 - Install Punch Windows | 5 | 0 | 24-Feb-14 A | 10-Mar-14 A | |
| L4-5130 | L4 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 12-Mar-14 A | |
| L5-5130 | L5 - Install Punch Windows | 5 | 0 | 10-Mar-14 A | 14-Mar-14 A | |
| L6-5130 | L6- Install Punch Windows | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L7-5130 | L7 - Install Punch Windows | 5 | 0 | 18-Mar-14 A | 21-Mar-14 A | |
| L8-5130 | L8 - Install Punch Windows | 5 | 0 | 24-Mar-14 A | 28-Mar-14 A | |
| L9-5130 | L9 - Install Punch Windows | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L10-5130 | L10 - Install Punch Windows | 5 | 0 | 08-Apr-14 A | 11-Apr-14 A | |
| L11-5130 | L11 - Install Punch Windows | 5 | 0 | 14-Apr-14 A | 21-Apr-14 A | |
| L12-5130 | L12 - Install Punch Windows | 5 | 0 | 22-Apr-14 A | 25-Apr-14 A | |
| L14-5130 | L14 - Install Punch Windows | 5 | 0 | 28-Apr-14 A | 05-May-14 A | |
| L15-5130 | L15 - Install Punch Windows | 5 | 0 | 09-May-14 A | 14-May-14 A | |
| L16-5130 | L16 - Install Punch Windows | 5 | 0 | 12-May-14 A | 20-May-14 A | |
| L17-5130 | L17 - Install Punch Windows | 5 | 0 | 27-May-14 A | 16-Jun-14 A | |

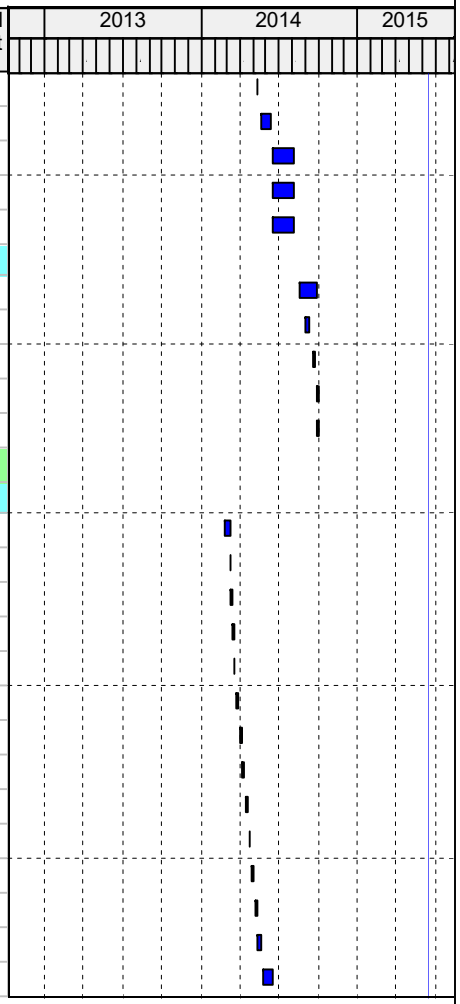



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| Roofs | | | | | | |
| **L1 - City Park Membrane - (elev 0')** | | | | | | |
| RF-4024 | L1 - City Park Roofing Membrane | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| RF-4026 | L1 - City Park - Protection Board | 3 | 0 | 22-Sep-14 A | 24-Sep-14 A | |
| RF-4028 | L1 - City Park - Gravel Fill | 2 | 0 | 25-Sep-14 A | 29-Sep-14 A | |
| **Pool Membrane - (elev 18')** | | | | | | |
| RF-4034 | Pool - Install plumbing | 3 | 0 | 20-Oct-14 A | 22-Oct-14 A | |
| **Lower Ballroom / Attic / Mech Roof - (elev 18')** | | | | | | |
| RF-4010 | AR - Set Mechanical Equipment | 5 | 0 | 10-Jun-14 A | 12-Jun-14 A | |
| RF-4006 | AR - Lower Ballroom / Attic Roofing System | 10 | 0 | 04-Aug-14 A | 27-Aug-14 A | |
| RF-4012 | L2.5 Horseshoe - Install corrugated metal panels | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| **Pool Green Roof - (elev 23')** | | | | | | |
| RF-4016 | RF - Pool Green Roofing System | 8 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| **Port Cochere / Entry Roof - (elev 23')** | | | | | | |
| PC-4008 | RF - Entry / Porte Cochere Roofing System | 5 | 0 | 29-Sep-14 A | 03-Oct-14 A | |
| **Upper Ballroom Roof - (elev 30')** | | | | | | |
| RF-4036 | RF - Upper Ballroom Roofing System | 3 | 0 | 28-Jul-14 A | 31-Jul-14 A | |
| **L3 - Pool Roof - (elev 40')** | | | | | | |
| RF-4014 | RF - Pool Roofing System | 4 | 0 | 31-Jul-14 A | 04-Aug-14 A | |
| **L12 - Terrace Green Roof - (elev 106')** | | | | | | |
| RF-4018 | TR - Terrace Roof - Green Roofing System | 5 | 0 | 10-Sep-14 A | 19-Sep-14 A | |
| RF-4020 | TR - Terrace Roof - Install sheet metal capping[DELE | 1 | 0 | 05-Dec-14 A | 05-Dec-14 A | |
| RF-4022 | TR - Terrace Roof - Install deocrative metal railing | 3 | 0 | 04-May-15 A | 05-May-15 A | |
| **L17 - Tower Roof - (elev 154')** | | | | | | |
| RF-4000 | Tower Roof - Roof Framing / Perimeter Framing / Sul | 10 | 0 | 02-Jun-14 A | 08-Jul-14 A | |
| RF-4002 | Tower Roof - Roofing System | 10 | 0 | 20-Aug-14 A | 17-Sep-14 A | |
| **PH - Roof - (elev 173')** | | | | | | |

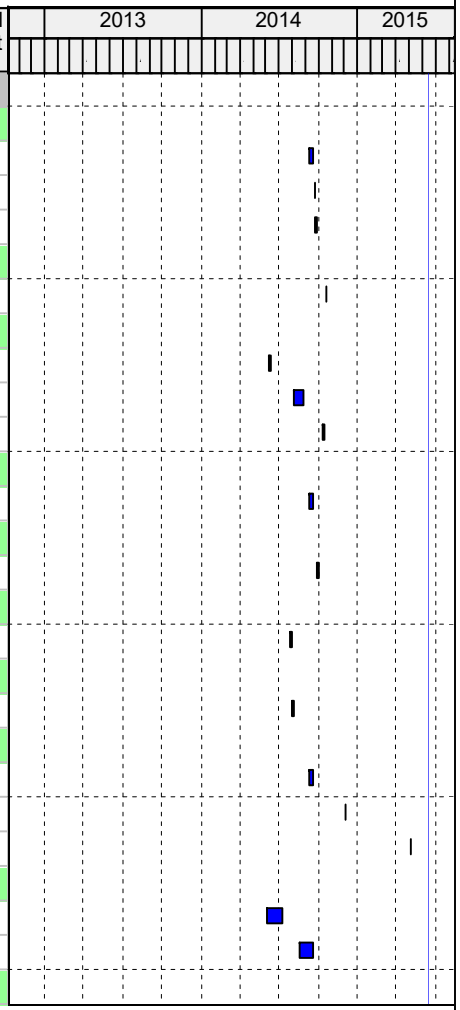



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| RF-4030 | PH - Roofing System | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| RF-4032 | PH - Coping / Flashing [DELETED] | 3 | 0 | 01-Sep-14 A | 01-Sep-14 A | |
| **Rough-In's** | | | | | | |
| Lower Podium - (Levels LL2 / LL1 / 1 / 2) | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| LL4-6002 | LL4 - Layout | 1 | 0 | 08-Nov-13 A | 08-Nov-13 A | |
| LL4-6008 | LL4 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL4-6012 | LL4 - Fire Sprinkler Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6014 | LL4 - Plumbing Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6018 | LL4 - HVAC Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL4-6004 | LL4 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL4-6016 | LL4 - Electrical Rl | 10 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6022 | LL4 - Fire Alarm / Elec Specialties Rl | 8 | 0 | 01-May-14 A | 21-Jul-14 A | |
| LL4-6010 | LL4 - Elevator pits | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| LL4-6020 | LL4 - H Mtl Frames | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| LL4-6006 | LL4 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL4-6024 | LL4 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 3 - (Parking)** | | | | | | |
| LL3-6002 | LL3 - Layout | 1 | 0 | 19-Nov-13 A | 19-Nov-13 A | |
| LL3-6008 | LL3 - Int Wall Framing | 5 | 0 | 09-Dec-13 A | 13-May-14 A | |
| LL3-6012 | LL3 - Fire Sprinkler Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6014 | LL3 - Plumbing Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6018 | LL3 - HVAC Rl | 10 | 0 | 16-Dec-13 A | 30-Dec-13 A | |
| LL3-6004 | LL3 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL3-6020 | LL3 - H Mtl Frames | 3 | 0 | 08-May-14 A | 09-May-14 A | |
| LL3-6010 | LL3 - F/P Curbs | 5 | 0 | 19-May-14 A | 19-May-14 A | |
| LL3-6016 | LL3 - Electrical Rl | 2 | 0 | 26-Jun-14 A | 21-Jul-14 A | |

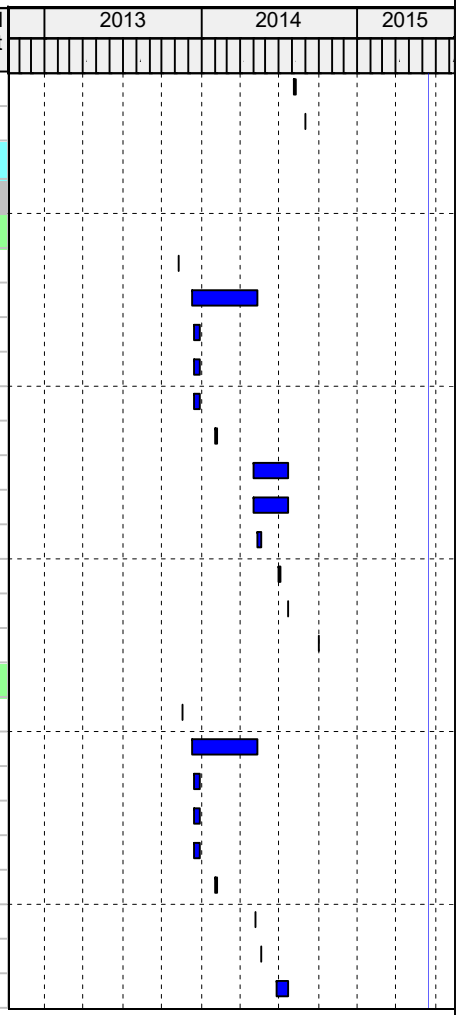



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-6022 | LL3 - Fire Alarm / Elec Specialties Rl | 8 | 0 | 26-Jun-14 A | 21-Jul-14 A | |
| LL3-6006 | LL3 - CMU Seismic Clips | 2 | 0 | 21-Jul-14 A | 21-Jul-14 A | |
| LL3-6024 | LL3 - Inspections | 2 | 0 | 03-Oct-14 A | 03-Oct-14 A | |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| LL2-6002 | LL2 - Layout | 1 | 0 | 14-Jan-14 A | 14-Jan-14 A | |
| LL2-6008 | LL2 - Int Wall Framing | 5 | 0 | 15-Jan-14 A | 21-Jan-14 A | |
| LL2-6012 | LL2 - Fire Sprinkler Rl | 10 | 0 | 21-Jan-14 A | 03-Feb-14 A | |
| LL2-6014 | LL2 - Plumbing Rl | 10 | 0 | 21-Jan-14 A | 14-Feb-14 A | |
| LL2E-6016 | LL2 - Electrical Rl | 8 | 0 | 03-Feb-14 A | 17-Mar-14 A | |
| LL2-6016 | LL2 - Electrical Rl | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2-6018 | LL2 - HVAC Rl | 10 | 0 | 03-Feb-14 A | 14-Feb-14 A | |
| LL2–6004 | LL2 - CMU Walls | 5 | 0 | 03-Feb-14 A | 07-Feb-14 A | |
| LL2E-6004 | LL2 - CMU Walls | 10 | 0 | 04-Mar-14 A | 09-May-14 A | |
| LL2E-6012 | LL2 - Fire Sprinkler Rl | 8 | 0 | 21-Mar-14 A | 01-Apr-14 A | |
| LL2-6030 | LL2 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 24-Apr-14 A | |
| LL2-6006 | LL2 - Ext Wall Framing - (Cold Formed) | 3 | 0 | 23-Apr-14 A | 21-Jul-14 A | |
| LL2E-6020 | LL2 - H Mtl Frames | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| LL2-6020 | LL2 - H Mtl Frames | 3 | 0 | 12-May-14 A | 13-May-14 A | |
| LL2E-6008 | LL2 - Int Wall Framing | 5 | 0 | 13-May-14 A | 22-Jun-14 A | |
| LL2E-6014 | LL2 - Plumbing Rl | 8 | 0 | 13-May-14 A | 30-May-14 A | |
| LL2E-6018 | LL2 - HVAC Rl | 8 | 0 | 13-May-14 A | 04-Aug-14 A | |
| LL2E-6022 | LL2 - Fire Alarm / Elec Specialties Rl (East of 10) | 8 | 0 | 13-May-14 A | 22-Sep-14 A | |
| LL2-6022 | LL2 - Fire Alarm / Elec Specialties Rl (West of 10) | 8 | 0 | 19-May-14 A | 22-Sep-14 A | |
| LL2-6015 | LL2 - Main Elect Room Set Equip / Rl - Power to Ma | 15 | 0 | 30-Jun-14 A | 26-Sep-14 A | |
| LL2-6028 | LL2 - CMU Seismic Clips | 4 | 0 | 16-Jul-14 A | 21-Jul-14 A | |
| LL2-6024 | LL2 - Inspections | 2 | 0 | 15-Sep-14 A | 03-Oct-14 A | |
| LL2-6010 | F/P Curbs at Garage | 3 | 3 | 17-Jun-15* | 19-Jun-15 | 2 |

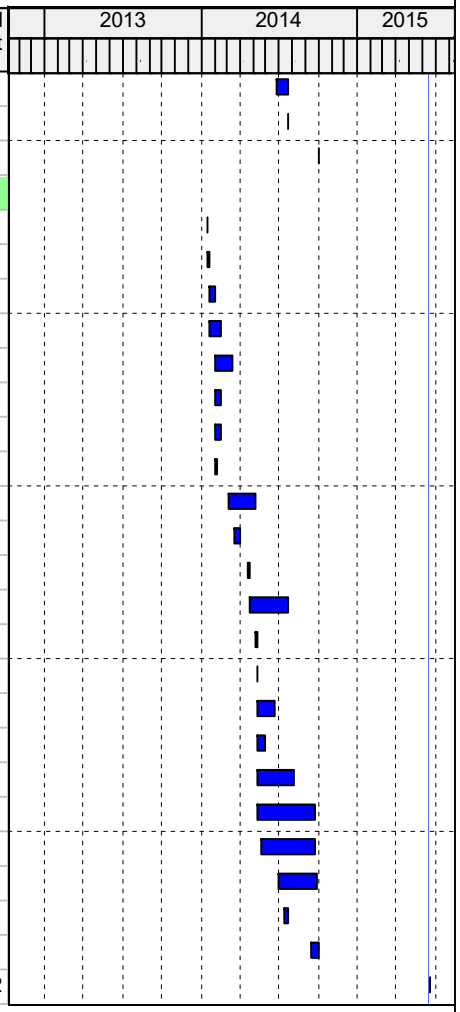


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |
| **All Areas** | | | | | | |
| LL1-6002 | Layout | 3 | 0 | 03-Jan-14 A | 08-Jan-14 A | |
| LL1-6008 | Int Wall Framing & Inspection | 6 | 0 | 08-Jan-14 A | 21-Jul-14 A | |
| LL1-Z2-6002 | Layout | 3 | 0 | 08-Jan-14 A | 14-Jan-14 A | |
| LL1-Z3-6002 | Layout | 3 | 0 | 14-Jan-14 A | 17-Jan-14 A | |
| LL1-Z2-6008 | Int Wall Framing & Inspection | 6 | 0 | 17-Jan-14 A | 01-Aug-14 A | |
| LL1-Z3-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-Jan-14 A | 04-Aug-14 A | |
| LL1-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 09-May-14 A | |
| LL1-Z2-6004 | CMU Walls | 3 | 0 | 03-Feb-14 A | 28-Apr-14 A | |
| LL1-Z3-6004 | CMU Walls (At All Areas North of Q-Line) | 3 | 0 | 03-Feb-14 A | 13-May-14 A | |
| LL1C-6012 | Complete Fire Sprinkler RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6016 | Complete Electrical RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 10 | 0 | 17-Feb-14 A | 16-Sep-14 A | |
| LL1C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 10 | 0 | 17-Feb-14 A | 12-Aug-14 A | |
| LL1-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 30-Apr-14 A | |
| LL1-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 22-Jul-14 A | |
| LL1-Z2-6012 | Fire Sprinkler RI | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z2-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z2-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 06-Aug-14 A | |
| LL1-Z3-6012 | Fire Sprinkler RI (At All Areas North of Q-Line) | 20 | 0 | 17-Feb-14 A | 03-Apr-14 A | |
| LL1-Z3-6014 | Plumbing RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |

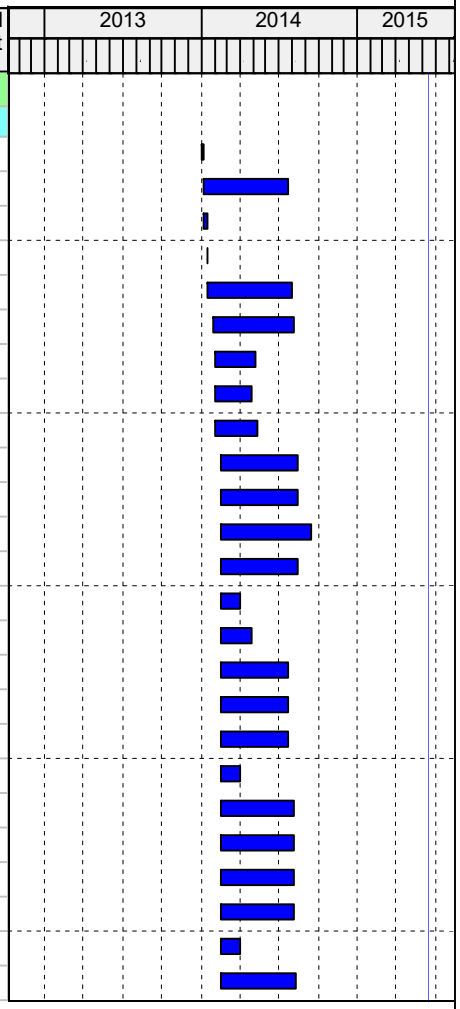



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3-6016 | Electrical RI | 20 | 0 | 17-Feb-14 A | 11-Sep-14 A | |
| LL1-Z3-6018 | HVAC RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z3-6022 | Fire Alarm / Elec Specialties RI | 20 | 0 | 17-Feb-14 A | 08-Aug-14 A | |
| LL1-Z2C-6012 | Complete Fire Sprinkler RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6014 | Complete Plumbing RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6016 | Complete Electrical RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2C-6018 | Complete HVAC RI @ Ceilings (delayed by remote da | 15 | 0 | 24-Feb-14 A | 15-Sep-14 A | |
| LL1-Z2C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 15 | 0 | 24-Feb-14 A | 21-Aug-14 A | |
| LL1-Z2-6020 | Hollow Metal Door Frames | 5 | 0 | 17-Mar-14 A | 04-Apr-14 A | |
| LL1-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| LL1-Z3-6020 | Hollow Metal Door Frames (At All Areas North of Q-Lir | 1 | 0 | 25-Mar-14 A | 04-Apr-14 A | |
| L1B-6004 | CMU Walls [including East Service Corridor] | 3 | 0 | 07-Apr-14 A | 10-Apr-14 A | |
| L1L-6002 | Layout [including back of house] | 3 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| LL1-6028 | LL1 - Erect HSS Perimeter Steel | 3 | 0 | 19-Apr-14 A | 29-Apr-14 A | |
| L1B-6008 | Int Wall Framing & Inspection | 6 | 0 | 21-Apr-14 A | 08-Aug-14 A | |
| LL1-6006 | LL1 - Ext Wall Framing / Furring - (Cold Formed) | 5 | 0 | 25-Apr-14 A | 21-Jul-14 A | |
| LL1C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 30-Apr-14 A | 30-Apr-14 A | |
| L1K-6004 | CMU Walls [including public restroom] | 3 | 0 | 05-May-14 A | 08-May-14 A | |
| L1K-6002 | Layout [including public restroom] | 3 | 0 | 08-May-14 A | 12-May-14 A | |
| L1K-6008 | Int Wall Framing & Inspection | 4 | 0 | 09-May-14 A | 22-Aug-14 A | |
| L1B-6002 | Layout [including East Service Corridor] | 3 | 0 | 14-May-14 A | 27-May-14 A | |
| L1L-6008 | Int Wall Framing & Inspection | 6 | 0 | 27-May-14 A | 06-Oct-14 A | |
| L1L-6004 | CMU Walls [including back of house] | 3 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L1K-6012 | Fire Sprinkler RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6014 | Plumbing RI | 10 | 0 | 02-Jun-14 A | 15-Sep-14 A | |
| L1K-6016 | Electrical RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |
| L1K-6018 | HVAC RI | 10 | 0 | 02-Jun-14 A | 29-Sep-14 A | |

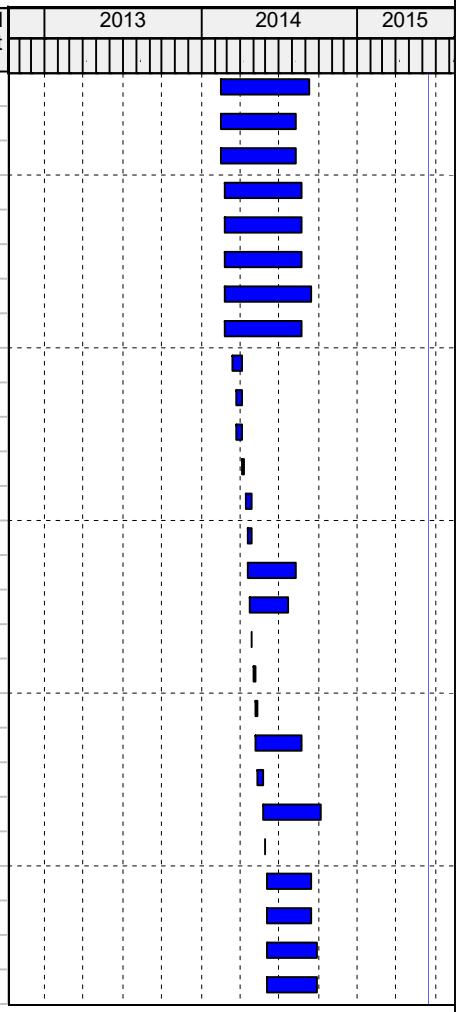



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1B-6014 | Plumbing RI [including East Service Corridor] | 10 | 0 | 16-Jun-14 A | 24-Jun-14 A | |
| L1B-6018 | HVAC RI | 10 | 0 | 20-Jun-14 A | 15-Aug-14 A | |
| L1B-6012 | Fire Sprinkler RI | 10 | 0 | 21-Jun-14 A | 15-Aug-14 A | |
| L1L-6018 | HVAC RI | 5 | 0 | 23-Jun-14 A | 13-Oct-14 A | |
| L1L-6014 | Plumbing RI | 5 | 0 | 24-Jun-14 A | 28-Oct-14 A | |
| L1L-6010 | CMU Seismic Clips [including back of house] [DELET | 2 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L1L-6012 | Fire Sprinkler RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |
| L1L-6016 | Electrical RI | 5 | 0 | 25-Jun-14 A | 13-Oct-14 A | |
| L1L-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 27-Jun-14 A | 13-Oct-14 A | |
| L1K-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 27-Jun-14 A | 29-Sep-14 A | |
| LL1-Z3-6009 | Frame Ceilings [DELETED] | 4 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L1B-6016 | Electrical RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| L1B-6022 | Fire Alarm / Elec Specialties RI | 10 | 0 | 07-Jul-14 A | 15-Aug-14 A | |
| LL1-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-Z2-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L1B-6010 | CMU Seismic Clips | 2 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| LL1-6024 | Inspections for Cover | 1 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L1B-6020 | Hollow Metal Door Frames | 5 | 0 | 01-Aug-14 A | 08-Aug-14 A | |
| LL1-Z3-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 04-Aug-14 A | |
| L1K-6010 | CMU Seismic Clips | 2 | 0 | 04-Aug-14 A | 06-Aug-14 A | |
| LL1-Z2-6024 | Inspections for Cover | 2 | 0 | 07-Aug-14 A | 08-Aug-14 A | |
| L1K-6020 | Hollow Metal Door Frames | 5 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| LL1-Z2-6009 | Frame Ceilings & Inspection | 6 | 0 | 22-Aug-14 A | 13-Oct-14 A | |
| L1L-6020 | Hollow Metal Door Frames | 5 | 0 | 25-Aug-14 A | 13-Oct-14 A | |
| LL1-6009 | Frame Ceilings & Inspection (except for bar redesign | 9 | 0 | 02-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3-6024 | Inspections for Cover | 2 | 0 | 12-Sep-14 A | 12-Sep-14 A | |
| LL1-Z3C-6012 | Complete Fire Sprinkler RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |

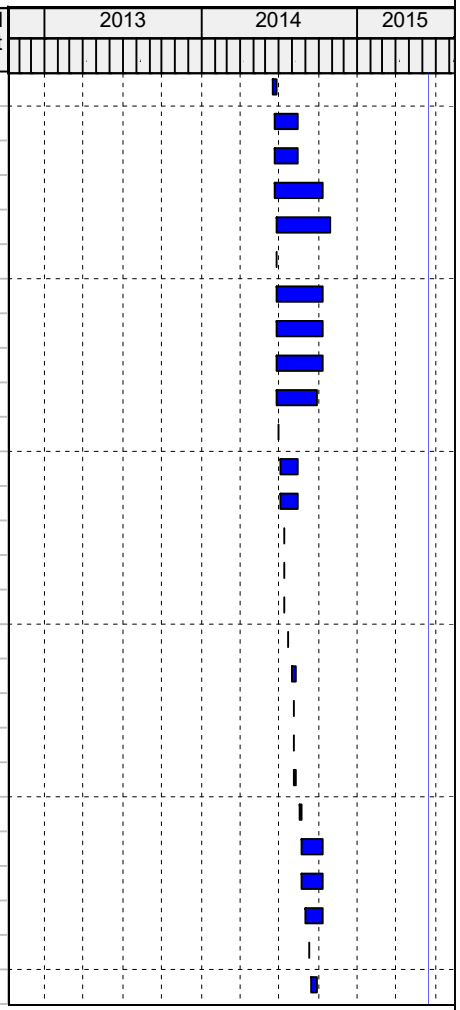


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-Z3C-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6016 | Complete Electrical RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| LL1-Z3C-6018 | Complete HVAC RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 29-Sep-14 A | |
| LL1-Z3C-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 5 | 0 | 15-Sep-14 A | 13-Oct-14 A | |
| L1KC-6012 | Complete Fire Sprinkler RI @ Ceilings & Inspection | 4 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L1B-6024 | Inspections for Cover (Main Ballroom N/S/W Walls & | 3 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1K-6024 | Inspections for Cover | 2 | 0 | 02-Oct-14 A | 03-Oct-14 A | |
| L1KC-6014 | Complete Plumbing RI @ Ceilings & Inspection | 4 | 0 | 02-Oct-14 A | 07-Oct-14 A | |
| L1BC-6014 | Complete Plumbing RI @ Ceilings | 7 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L1KC-6018 | Complete HVAC RI @ Ceilings & Inspection | 4 | 0 | 06-Oct-14 A | 10-Nov-14 A | |
| L1KC-6016 | Complete Electrical RI @ Ceilings & Inspection | 3 | 0 | 20-Oct-14 A | 10-Nov-14 A | |
| L1KC-6022 | Complete Fire Alarm / Elec Specialties RI @ Ceilings | 3 | 0 | 20-Oct-14 A | 10-Nov-14 A | |
| L1L-6024 | Inspections for Cover | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L1L-6009 | Frame ceilings & inspection at high ceiling | 13 | 0 | 24-Nov-14 A | 20-Jan-15 A | |
| L1B-6009 | Frame Ceilings & inspection at Main Ballroom (per re | 5 | 0 | 04-Dec-14 A | 16-Jan-15 A | |
| L1LC-6012 | Complete fire sprinkler RI @ ceilings | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1LC-6014 | Complete Plumbing RI @ Ceilings | 5 | 0 | 05-Jan-15 A | 07-Jan-15 A | |
| L1LC-6016 | Complete electrical rough-in @ ceilings & inspection | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1LC-6018 | Complete HVAC RI @ Ceilings | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1LC-6022 | Complete fire alarm/elec specialties RI @ ceilings & ir | 5 | 0 | 05-Jan-15 A | 26-Jan-15 A | |
| L1K-6009 | Frame ceilings & inspection at public restroom | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L1B-8118 | Lighting & electrical trim at Ballrooms | 7 | 0 | 07-Apr-15 A | 17-Apr-15 A | |
| L1B-8112 | Fire sprinkler trim at Ballrooms | 2 | 0 | 13-Apr-15 A | 14-Apr-15 A | |
| L1B-8204 | HVAC trim at Ballrooms | 5 | 0 | 13-Apr-15 A | 15-Apr-15 A | |
| L1BC-6022 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 13-Apr-15 A | 14-Apr-15 A | |
| **Level 1 - (Lobby / Dining / Kitchen / Main Ballrooms)** | | | | | | |
| L01-6028 | L1 - Erect HSS Perimeter Steel | 5 | 0 | 17-Apr-14 A | 09-May-14 A | |

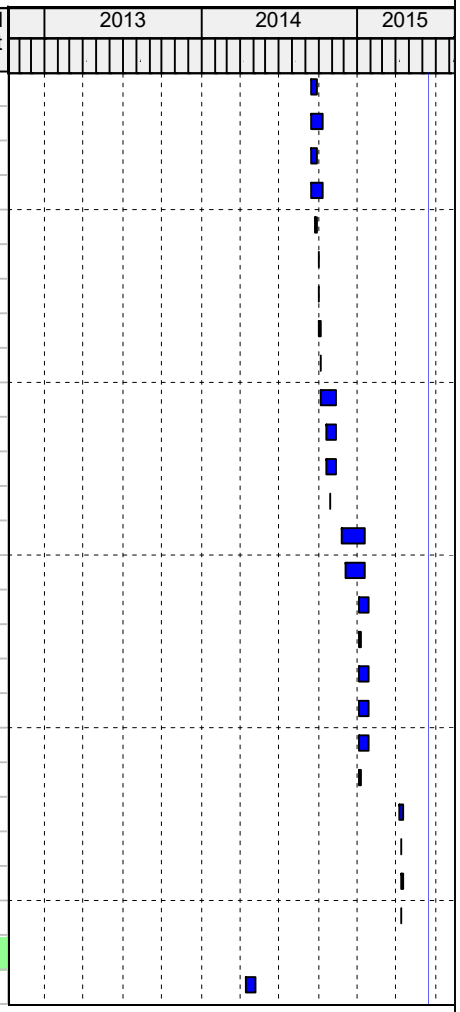



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **Level 2 - (Admin / Employee Ares)** | | | | | | |
| L02-6006 | L2 - Support Frame/Sheathing for Metal Panels | 6 | 0 | 23-Apr-14 A | 07-Aug-14 A | |
| L02-6008 | L2 - Int Wall Framing | 10 | 0 | 25-Apr-14 A | 17-Jul-14 A | |
| L02-6014 | L2 - Plumbing RI | 15 | 0 | 28-Apr-14 A | 07-Aug-14 A | |
| L02-6028 | L2 - Erect HSS Perimeter Steel | 5 | 0 | 28-Apr-14 A | 09-May-14 A | |
| L02-6004 | L2 - CMU Walls | 5 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L02-6002 | L2 - Layout | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L02-6010 | L2 - CMU Seismic Clips | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L02-6018 | L2 - HVAC RI (including equipment) | 20 | 0 | 18-Jun-14 A | 10-Sep-14 A | |
| L02-6016 | L2 - Electrical RI | 10 | 0 | 24-Jun-14 A | 14-Aug-14 A | |
| L02-6022 | L2 - Fire Alarm / Elec Specialties RI | 10 | 0 | 24-Jun-14 A | 10-Oct-14 A | |
| L02-6012 | L2 - Fire Sprinkler RI | 10 | 0 | 26-Jun-14 A | 07-Aug-14 A | |
| L02-6020 | L2 - H Mtl Frames | 5 | 0 | 11-Jul-14 A | 17-Jul-14 A | |
| L02-6024 | L2 - Inspections - North Half | 2 | 0 | 10-Oct-14 A | 20-Oct-14 A | |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| L04-6012 | Fire Sprinkler Mains | 5 | 0 | 01-Feb-14 A | 03-Apr-14 A | |
| L03-8219 | HVAC Risers | 5 | 0 | 11-Feb-14 A | 23-Mar-14 A | |
| L03-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 11-Feb-14 A | 03-Mar-14 A | |
| L03-6002 | Layout | 5 | 0 | 13-Feb-14 A | 19-Feb-14 A | |
| L04-8219 | HVAC Risers | 5 | 0 | 13-Feb-14 A | 23-Mar-14 A | |
| L05-8219 | HVAC Risers | 5 | 0 | 17-Feb-14 A | 03-Mar-14 A | |
| L03-6008 | Frame Shaft Walls | 3 | 0 | 18-Feb-14 A | 26-Mar-14 A | |
| L04-6002 | Layout | 5 | 0 | 19-Feb-14 A | 25-Feb-14 A | |
| L04-6008 | Frame Shaft Walls | 3 | 0 | 20-Feb-14 A | 26-Mar-14 A | |
| L03-6011 | PreRock Shafts | 2 | 0 | 24-Feb-14 A | 25-Mar-14 A | |
| L03-6010 | Frame Walls | 5 | 0 | 25-Feb-14 A | 25-Mar-14 A | |

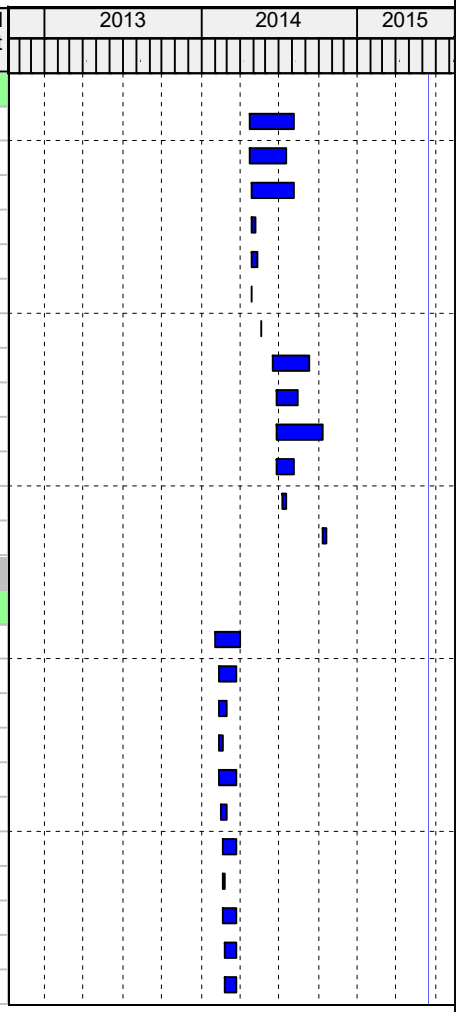


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6002 | Layout | 5 | 0 | 27-Feb-14 A | 03-Mar-14 A | |
| L04-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 28-Feb-14 A | 05-Mar-14 A | |
| L03-6016 | Electrical RI | 5 | 0 | 03-Mar-14 A | 04-Apr-14 A | |
| L03-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 12-Mar-14 A | |
| L04-6009 | Inspect Shafts | 1 | 0 | 03-Mar-14 A | 13-Mar-14 A | |
| L04-6010 | Frame Walls | 5 | 0 | 04-Mar-14 A | 05-Jun-14 A | |
| L05-6008 | Frame Shaft Walls | 3 | 0 | 05-Mar-14 A | 27-Mar-14 A | |
| L06-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L07-8219 | HVAC Risers | 5 | 0 | 05-Mar-14 A | 01-Apr-14 A | |
| L05-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 06-Mar-14 A | 21-Mar-14 A | |
| L03-6020 | Install Hollow Metal Frames | 3 | 0 | 12-Mar-14 A | 21-Mar-14 A | |
| L04-6020 | Install Hollow Metal Frames | 3 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L05-6010 | Frame Walls | 5 | 0 | 14-Mar-14 A | 21-Mar-14 A | |
| L06-6002 | Layout | 5 | 0 | 14-Mar-14 A | 18-Mar-14 A | |
| L04-6011 | PreRock Shafts | 2 | 0 | 18-Mar-14 A | 25-Mar-14 A | |
| L05-6009 | Inspect Shafts | 1 | 0 | 18-Mar-14 A | 18-Mar-14 A | |
| L05-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 21-Mar-14 A | |
| L06-6008 | Frame Shaft Walls | 3 | 0 | 19-Mar-14 A | 03-Apr-14 A | |
| L06-6020 | Install Hollow Metal Frames | 3 | 0 | 19-Mar-14 A | 27-Mar-14 A | |
| L04-6016 | Electrical RI | 5 | 0 | 20-Mar-14 A | 09-Apr-14 A | |
| L05-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 26-Mar-14 A | |
| L06-6011 | PreRock Shafts | 2 | 0 | 21-Mar-14 A | 07-Apr-14 A | |
| L07-6002 | Layout | 5 | 0 | 24-Mar-14 A | 30-Apr-14 A | |
| L03-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L03-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |
| L04-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 25-Mar-14 A | 25-Mar-14 A | |

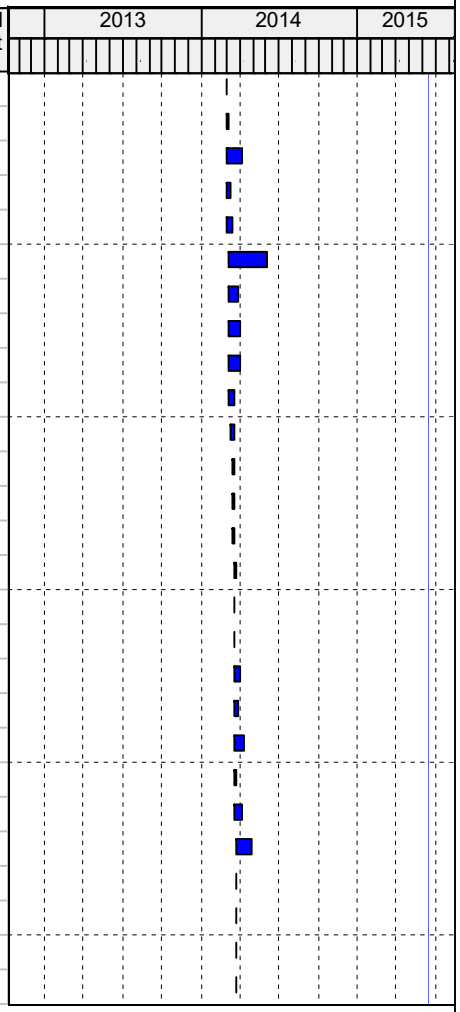



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-6016 | Electrical RI | 5 | 0 | 25-Mar-14 A | 05-Jun-14 A | |
| L04-6019 | Complete Top Out GWB | 2 | 0 | 26-Mar-14 A | 06-Jun-14 A | |
| L05-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 26-Mar-14 A | 26-Mar-14 A | |
| L06-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 26-Mar-14 A | 01-Apr-14 A | |
| L03-6019 | Complete Top Out GWB | 2 | 0 | 27-Mar-14 A | 02-May-14 A | |
| L08-6002 | Layout | 5 | 0 | 27-Mar-14 A | 02-Apr-14 A | |
| L05-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 28-Mar-14 A | 03-Apr-14 A | |
| L06-6010 | Frame Walls | 5 | 0 | 28-Mar-14 A | 07-Apr-14 A | |
| L03-6012 | Fire Sprinkler Mains | 5 | 0 | 31-Mar-14 A | 04-Apr-14 A | |
| L07-6008 | Frame Shaft Walls | 3 | 0 | 31-Mar-14 A | 03-Apr-14 A | |
| L05-6019 | Complete Top Out GWB | 2 | 0 | 01-Apr-14 A | 08-Apr-14 A | |
| L07-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 01-Apr-14 A | 11-Apr-14 A | |
| L08-6008 | Frame Shaft Walls | 3 | 0 | 02-Apr-14 A | 21-Apr-14 A | |
| L03-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L04-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L05-6023 | Inspection of Exterior Framing | 0 | 0 | 03-Apr-14 A | | |
| L06-6016 | Electrical RI | 5 | 0 | 03-Apr-14 A | 15-Apr-14 A | |
| L07-6009 | Inspect Shafts | 1 | 0 | 03-Apr-14 A | 03-Apr-14 A | |
| L07-6011 | PreRock Shafts | 2 | 0 | 03-Apr-14 A | 07-Apr-14 A | |
| L05-6012 | Fire Sprinkler Mains | 5 | 0 | 04-Apr-14 A | 30-Apr-14 A | |
| L06-6012 | Fire Sprinkler Mains | 5 | 0 | 07-Apr-14 A | 30-Apr-14 A | |
| L06-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L06-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L07-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 07-Apr-14 A | 08-Apr-14 A | |
| L07-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 07-Apr-14 A | 07-Apr-14 A | |
| L03-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L03-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |

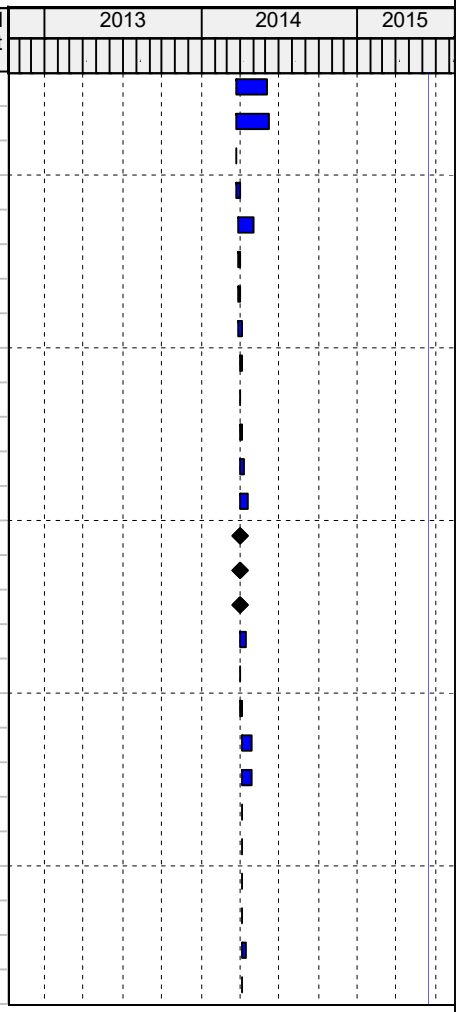



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 08-Apr-14 A | 17-Apr-14 A | |
| L06-6009 | Inspect Shafts | 1 | 0 | 08-Apr-14 A | 08-Apr-14 A | |
| L06-6019 | Complete Top Out GWB | 2 | 0 | 08-Apr-14 A | 18-Apr-14 A | |
| L07-6010 | Frame Walls | 5 | 0 | 08-Apr-14 A | 15-Apr-14 A | |
| L08-6011 | PreRock Shafts | 2 | 0 | 08-Apr-14 A | 23-Apr-14 A | |
| L09-6002 | Layout | 5 | 0 | 08-Apr-14 A | 26-Apr-14 A | |
| L03-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 09-Apr-14 A | 08-May-14 A | |
| L03-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 09-Apr-14 A | 09-Apr-14 A | |
| L05-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 09-Apr-14 A | 14-Apr-14 A | |
| L08-6009 | Inspect Shafts | 1 | 0 | 09-Apr-14 A | 25-Apr-14 A | |
| L09-6008 | Frame Shaft Walls | 3 | 0 | 11-Apr-14 A | 15-Apr-14 A | |
| L08-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 14-Apr-14 A | 25-Apr-14 A | |
| L04-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 15-Apr-14 A | 16-Apr-14 A | |
| L07-6012 | Fire Sprinkler Mains | 5 | 0 | 15-Apr-14 A | 30-Apr-14 A | |
| L07-6016 | Electrical RI | 5 | 0 | 15-Apr-14 A | 12-May-14 A | |
| L07-6020 | Install Hollow Metal Frames | 3 | 0 | 16-Apr-14 A | 23-Apr-14 A | |
| L05-6025 | Inst Thermal & VB @ Exterior Walls (App to cover 4' | 1 | 0 | 17-Apr-14 A | 25-Apr-14 A | |
| L06-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 17-Apr-14 A | 12-May-14 A | |
| L06-6023 | Inspection of Exterior Framing | 0 | 0 | 17-Apr-14 A | | |
| L09-8219 | HVAC Risers | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L09-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 17-Apr-14 A | 21-Apr-14 A | |
| L04-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 18-Apr-14 A | 20-Apr-14 A | |
| L04-6028 | PreRock at Heat Pumps | 2 | 0 | 20-Apr-14 A | 22-Apr-14 A | |
| L08-8219 | HVAC Risers | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-8220 | Plumbing Mains/Risers/Overhead | 5 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L08-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |
| L09-6009 | Inspect Shafts | 1 | 0 | 21-Apr-14 A | 21-Apr-14 A | |

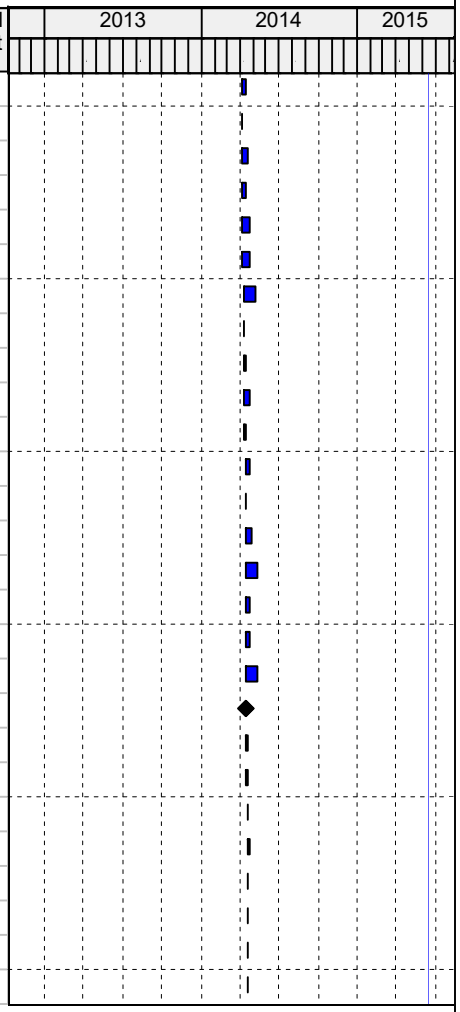



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L09-6011 | PreRock Shafts | 2 | 0 | 22-Apr-14 A | 24-Apr-14 A | |
| L04-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Apr-14 A | 23-Apr-14 A | |
| L06-6025 | Inst Thermal & VB @ Corners (App to cover 4' of De | 1 | 0 | 23-Apr-14 A | 25-Apr-14 A | |
| L08-6020 | Install Hollow Metal Frames | 3 | 0 | 23-Apr-14 A | 13-May-14 A | |
| L11-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L11-8220 | Plumbing Risers - Install | 2 | 0 | 23-Apr-14 A | 24-Apr-14 A | |
| L04-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L09-6017 | Firetape/Caulk @ Shafts | 1 | 0 | 24-Apr-14 A | 24-Apr-14 A | |
| L10-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L10-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 20-May-14 A | |
| L12-8220 | Plumbing Risers - Install | 2 | 0 | 24-Apr-14 A | 25-Apr-14 A | |
| L04-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 25-Apr-14 A | 11-Jun-14 A | |
| L04-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L09-6010 | Frame Walls | 5 | 0 | 25-Apr-14 A | 20-May-14 A | |
| L09-6015 | Inspect Pre Rock @ Shafts | 1 | 0 | 25-Apr-14 A | 25-Apr-14 A | |
| L10-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L11-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 25-Apr-14 A | 30-Apr-14 A | |
| L12-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 25-Apr-14 A | 28-Apr-14 A | |
| L08-6010 | Frame Walls | 5 | 0 | 26-Apr-14 A | 30-Apr-14 A | |
| L10-6002 | Layout | 5 | 0 | 27-Apr-14 A | 27-Apr-14 A | |
| L04-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 28-Apr-14 A | 30-Apr-14 A | |
| L05-6018 | HVAC RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Apr-14 A | 05-Jun-14 A | |
| L05-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L06-6028 | PreRock at Heat Pumps | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L07-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 28-Apr-14 A | 12-May-14 A | |

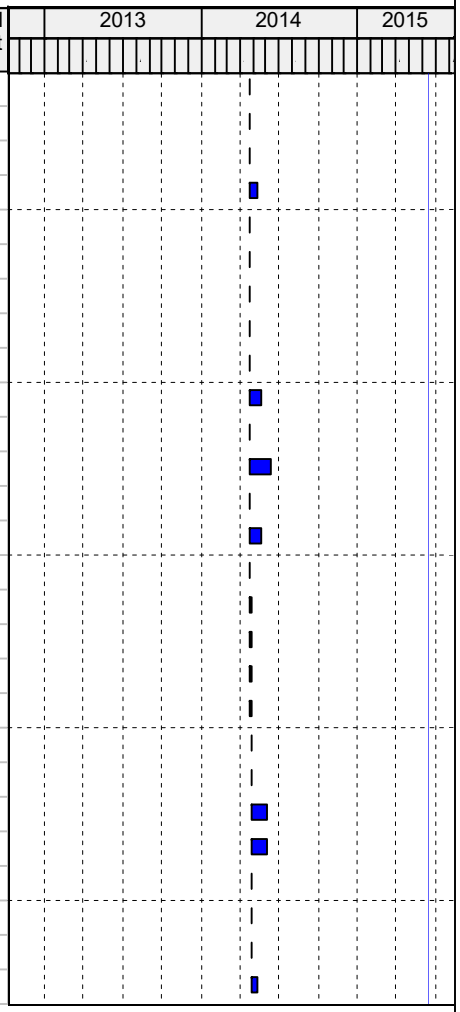



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-Apr-14 A | 22-May-14 A | |
| L11-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L12-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-Apr-14 A | 29-Apr-14 A | |
| L12-6002 | Layout | 5 | 0 | 28-Apr-14 A | 28-Apr-14 A | |
| L05-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 13-May-14 A | |
| L05-6028 | PreRock at Heat Pumps | 2 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L05-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L06-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 29-Apr-14 A | 09-May-14 A | |
| L06-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 29-Apr-14 A | 29-Apr-14 A | |
| L06-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 30-Apr-14 A | |
| L07-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L08-6019 | Complete Top Out GWB | 2 | 0 | 29-Apr-14 A | 12-May-14 A | |
| L08-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L09-6020 | Install Hollow Metal Frames | 3 | 0 | 29-Apr-14 A | 20-May-14 A | |
| L09-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L10-6023 | Inspection of Exterior Framing | 0 | 0 | 29-Apr-14 A | | |
| L04-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 30-Apr-14 A | 02-May-14 A | |
| L09-6019 | Complete Top Out GWB | 2 | 0 | 30-Apr-14 A | 06-Jun-14 A | |
| L11-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L12-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-Apr-14 A | 22-May-14 A | |
| L03-6028 | PreRock at Heat Pumps | 2 | 0 | 01-May-14 A | 02-May-14 A | |
| L05-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L06-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 01-May-14 A | 02-May-14 A | |
| L03-6014 | Set Tubs & Plumbing RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |
| L03-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 02-May-14 A | 08-May-14 A | |

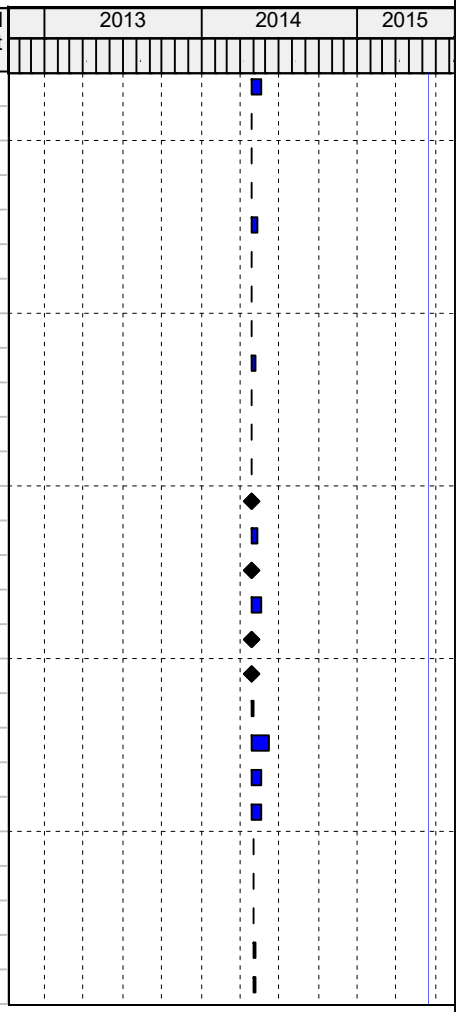



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L03-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 05-May-14 A | 05-May-14 A | |
| L05-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L05-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 07-May-14 A | |
| L06-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-May-14 A | 09-May-14 A | |
| L06-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 05-May-14 A | 09-May-14 A | |
| L03-6018 | HVAC RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L03-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 06-May-14 A | 06-May-14 A | |
| L07-6014 | Set Tubs & Plumbing RI | 5 | 0 | 06-May-14 A | 12-May-14 A | |
| L07-6221 | Frame Ceilings & Furring Walls | 3 | 0 | 06-May-14 A | 09-May-14 A | |
| L03-6004 | CMU Wall/Clips | 3 | 0 | 07-May-14 A | 08-May-14 A | |
| L03-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-May-14 A | 07-May-14 A | |
| L03-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 08-May-14 A | 13-May-14 A | |
| L03-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6004 | CMU Walls | 3 | 0 | 09-May-14 A | 12-May-14 A | |
| L04-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6018 | HVAC RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L04-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L06-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-May-14 A | 13-May-14 A | |
| L11-6010 | Frame Walls | 5 | 0 | 09-May-14 A | 15-May-14 A | |
| L05-6014 | Set Tubs & Plumbing RI | 5 | 0 | 12-May-14 A | 05-Jun-14 A | |
| L07-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 12-May-14 A | 13-May-14 A | |
| L11-6020 | Install Hollow Metal Frames | 3 | 0 | 12-May-14 A | 14-May-14 A | |
| L11-6019 | Complete Top Out GWB | 2 | 0 | 12-May-14 A | 14-May-14 A | |
| L14-6002 | Layout | 5 | 0 | 12-May-14 A | 14-May-14 A | |
| L15-6002 | Layout | 5 | 0 | 12-May-14 A | 15-May-14 A | |
| L05-6004 | CMU Walls | 3 | 0 | 13-May-14 A | 13-May-14 A | |
| L06-6018 | HVAC RI | 5 | 0 | 13-May-14 A | 25-Jun-14 A | |

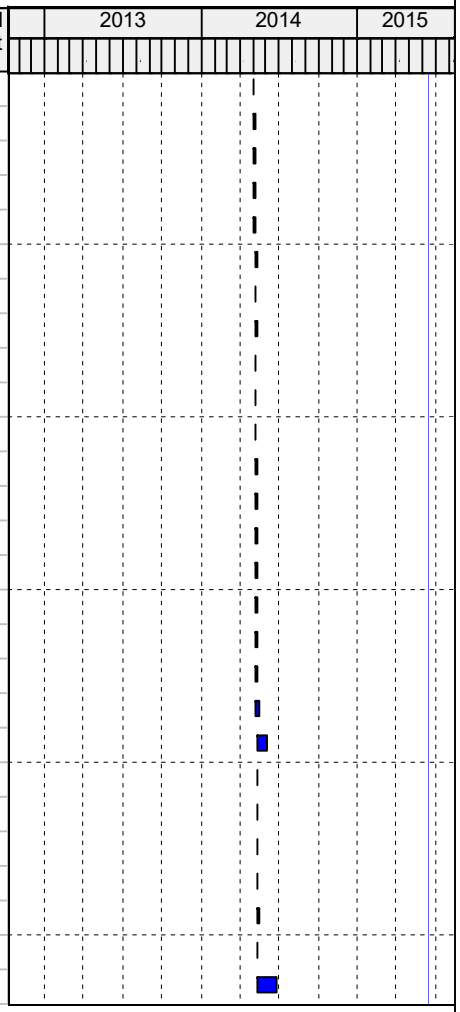



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 13-May-14 A | 14-Jul-14 A | |
| L07-6018 | HVAC Rl | 5 | 0 | 13-May-14 A | 05-Jun-14 A | |
| L07-6022 | Fire Alarm / Elec Specialties Rl | 5 | 0 | 13-May-14 A | 21-May-14 A | |
| L07-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 13-May-14 A | 13-May-14 A | |
| L14-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 13-May-14 A | 14-May-14 A | |
| L16-6002 | Layout | 5 | 0 | 13-May-14 A | 16-May-14 A | |
| L06-6004 | CMU Walls | 3 | 0 | 14-May-14 A | 14-May-14 A | |
| L07-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 15-May-14 A | |
| L08-6012 | Fire Sprinkler Mains | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6004 | CMU Walls | 3 | 0 | 15-May-14 A | 20-May-14 A | |
| L17-6002 | Layout | 5 | 0 | 15-May-14 A | 20-May-14 A | |
| L07-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L08-6014 | Set Tubs & Plumbing Rl | 5 | 0 | 16-May-14 A | 25-Jun-14 A | |
| L08-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6004 | CMU Walls | 3 | 0 | 16-May-14 A | 16-May-14 A | |
| L09-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-May-14 A | 16-May-14 A | |
| L11-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L12-6023 | Inspection of Exterior Framing | 0 | 0 | 16-May-14 A | | |
| L07-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L08-6028 | PreRock at Heat Pumps | 2 | 0 | 19-May-14 A | 20-May-14 A | |
| L09-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-May-14 A | 19-May-14 A | |
| L10-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L11-6004 | CMU Walls | 3 | 0 | 19-May-14 A | 19-May-14 A | |
| L15-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 19-May-14 A | 19-May-14 A | |
| L07-6028 | PreRock at Heat Pumps | 2 | 0 | 20-May-14 A | 21-May-14 A | |
| L07-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 20-May-14 A | 20-May-14 A | |

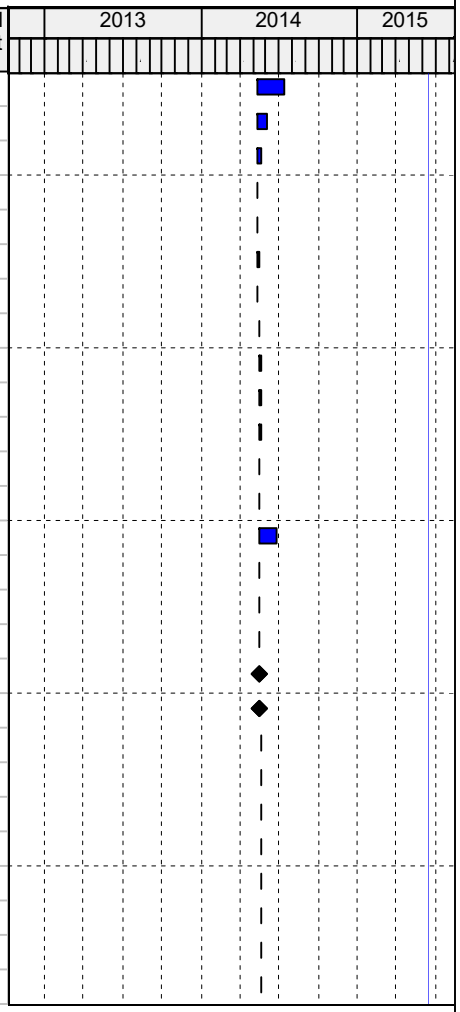



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 20-May-14 A | 21-May-14 A | |
| L10-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L11-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L12-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-May-14 A | 20-May-14 A | |
| L14-6004 | CMU Walls | 3 | 0 | 20-May-14 A | 20-May-14 A | |
| L07-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 21-May-14 A | 27-May-14 A | |
| L08-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L08-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L09-6028 | PreRock at Heat Pumps | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L10-6014 | Set Tubs & Plumbing RI | 5 | 0 | 21-May-14 A | 27-Jun-14 A | |
| L10-6010 | Frame Walls | 5 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6019 | Complete Top Out GWB | 2 | 0 | 21-May-14 A | 03-Jun-14 A | |
| L10-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L11-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L12-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 21-May-14 A | 21-May-14 A | |
| L14-8220 | Plumbing Risers - Install | 2 | 0 | 21-May-14 A | 22-May-14 A | |
| L15-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L16-6004 | CMU Walls | 3 | 0 | 21-May-14 A | 21-May-14 A | |
| L07-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-May-14 A | 23-May-14 A | |
| L08-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 22-May-14 A | 22-May-14 A | |
| L10-6012 | Fire Sprinkler Mains | 5 | 0 | 22-May-14 A | 27-May-14 A | |
| L08-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L09-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-May-14 A | 23-May-14 A | |
| L10-6020 | Install Hollow Metal Frames | 3 | 0 | 23-May-14 A | 03-Jun-14 A | |
| L10-6028 | PreRock at Heat Pumps | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L14-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 23-May-14 A | 27-May-14 A | |

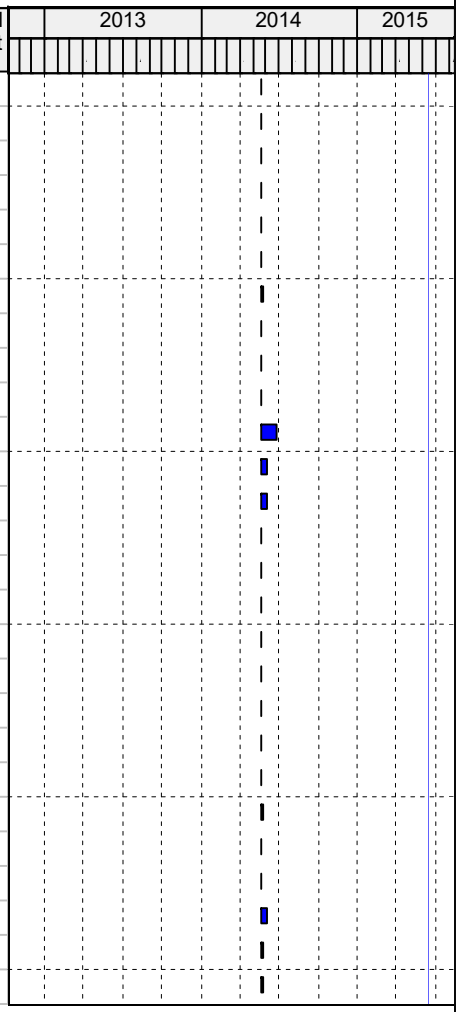



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8220 | Plumbing Risers - Install | 2 | 0 | 23-May-14 A | 27-May-14 A | |
| L09-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 27-May-14 A | 27-May-14 A | |
| L12-6010 | Frame Walls | 5 | 0 | 27-May-14 A | 02-Jun-14 A | |
| L08-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L09-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 28-May-14 A | 28-May-14 A | |
| L10-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 28-May-14 A | 03-Jun-14 A | |
| L14-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 28-May-14 A | 02-Jun-14 A | |
| L15-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 28-May-14 A | 30-May-14 A | |
| L16-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 28-May-14 A | 28-May-14 A | |
| L16-8220 | Plumbing Risers - Install | 2 | 0 | 28-May-14 A | 29-May-14 A | |
| L08-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 29-May-14 A | 30-May-14 A | |
| L10-6016 | Electrical RI | 5 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 29-May-14 A | 08-Aug-14 A | |
| L10-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L10-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 30-May-14 A | 30-May-14 A | |
| L12-6012 | Fire Sprinkler Mains | 5 | 0 | 30-May-14 A | 26-Jun-14 A | |
| L12-6020 | Install Hollow Metal Frames | 3 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L15-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 30-May-14 A | 03-Jun-14 A | |
| L17-8219 | HVAC Risers - Install & Inspect | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L17-8220 | Plumbing Risers - Install | 2 | 0 | 30-May-14 A | 02-Jun-14 A | |
| L10-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L11-6016 | Electrical RI | 5 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L11-6022 | Fire Alarm / Elec Specialties RI | 4 | 0 | 02-Jun-14 A | 13-Aug-14 A | |
| L12-6019 | Complete Top Out GWB | 2 | 0 | 02-Jun-14 A | 03-Jun-14 A | |
| L14-6020 | Install Hollow Metal Frames | 3 | 0 | 02-Jun-14 A | 05-Jun-14 A | |
| L14-6010 | Frame Walls | 5 | 0 | 02-Jun-14 A | 04-Jun-14 A | |
| L16-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 02-Jun-14 A | 02-Jun-14 A | |

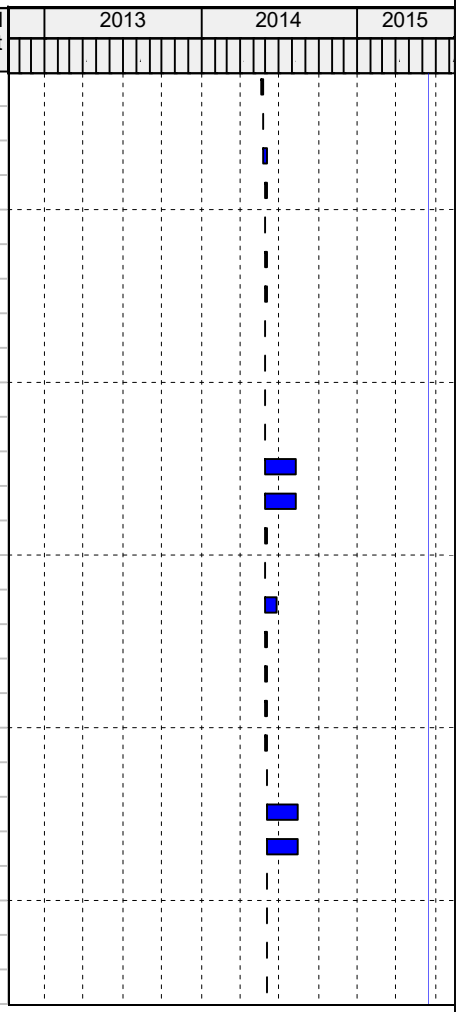



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L14-6019 | Complete Top Out GWB | 2 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L16-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 03-Jun-14 A | 05-Jun-14 A | |
| L10-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 04-Jun-14 A | 04-Jun-14 A | |
| L17-6008 | Frame Shaft Walls & Inspect (Part 1) | 2 | 0 | 04-Jun-14 A | 11-Jun-14 A | |
| L08-6016 | Electrical RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L08-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 05-Jun-14 A | 14-Jul-14 A | |
| L09-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L12-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 05-Jun-14 A | 10-Jun-14 A | |
| L15-6010 | Frame Walls | 3 | 0 | 05-Jun-14 A | 11-Jun-14 A | |
| L09-6012 | Fire Sprinkler Mains | 5 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L09-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L11-6012 | Fire Sprinkler Mains | 4 | 0 | 06-Jun-14 A | 09-Jun-14 A | |
| L12-6014 | Set Tubs & Plumbing RI | 4 | 0 | 06-Jun-14 A | 27-Jun-14 A | |
| L11-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jun-14 A | 11-Jun-14 A | |
| L09-6014 | Set Tubs & Plumbing RI | 5 | 0 | 09-Jun-14 A | 25-Jun-14 A | |
| L14-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L15-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L16-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 09-Jun-14 A | 11-Jun-14 A | |
| L09-6016 | Electrical RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 10-Jun-14 A | 05-Aug-14 A | |
| L09-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6013 | Fire Sprinkler Branch Lines | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L14-6014 | Set Tubs & Plumbing RI | 4 | 0 | 10-Jun-14 A | 21-Jul-14 A | |
| L15-6020 | Install Hollow Metal Frames | 3 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L15-6019 | Complete Top Out GWB | 2 | 0 | 10-Jun-14 A | 11-Jun-14 A | |
| L11-6014 | Set Tubs & Plumbing RI | 4 | 0 | 11-Jun-14 A | 26-Jun-14 A | |
| L11-6028 | PreRock at Heat Pumps | 2 | 0 | 13-Jun-14 A | 14-Jun-14 A | |

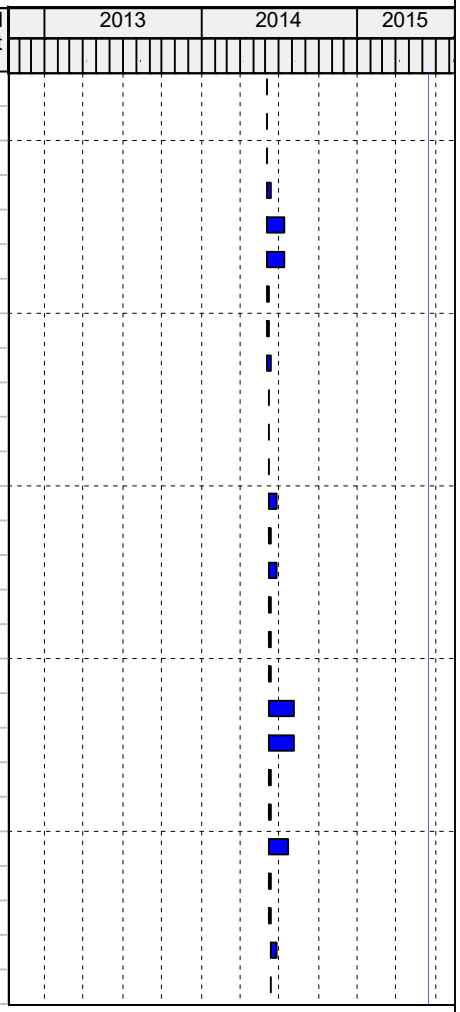



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 14-Jun-14 A | 14-Jun-14 A | |
| L14-6012 | Fire Sprinkler Mains | 2 | 0 | 16-Jun-14 A | 27-Jun-14 A | |
| L14-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 18-Jun-14 A | 18-Jun-14 A | |
| L15-6023 | Inspection of Exterior Framing | 0 | 0 | 18-Jun-14 A | | |
| L17-6009 | PreRock Shafts (2 Layers) & Inspect (Part 1) | 4 | 0 | 18-Jun-14 A | 23-Jun-14 A | |
| L17-6010 | Frame Walls | 5 | 0 | 18-Jun-14 A | 29-Jul-14 A | |
| L10-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L12-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6028 | PreRock at Heat Pumps | 2 | 0 | 19-Jun-14 A | 19-Jun-14 A | |
| L14-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 19-Jun-14 A | 20-Jun-14 A | |
| L14-6023 | Inspection of Exterior Framing | 0 | 0 | 20-Jun-14 A | | |
| L15-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 20-Jun-14 A | 20-Jun-14 A | |
| L10-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 22-Jun-14 A | 23-Jun-14 A | |
| L15-6014 | Set Tubs & Plumbing RI | 5 | 0 | 22-Jun-14 A | 24-Jul-14 A | |
| L08-6018 | HVAC RI | 3 | 0 | 23-Jun-14 A | 25-Jun-14 A | |
| L12-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L14-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L15-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 23-Jun-14 A | 23-Jun-14 A | |
| L08-6221 | Frame Unit Ceilings | 2 | 0 | 24-Jun-14 A | 25-Jun-14 A | |
| L11-6019HP | Install Heat Pumps & Connect to Floor Below | 4 | 0 | 24-Jun-14 A | 27-Jun-14 A | |
| L12-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L14-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Jun-14 A | 24-Jun-14 A | |
| L17-6023 | Inspection of Exterior Framing | 0 | 0 | 24-Jun-14 A | | |
| L12-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| L12-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |
| L14-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 25-Jun-14 A | 27-Jun-14 A | |

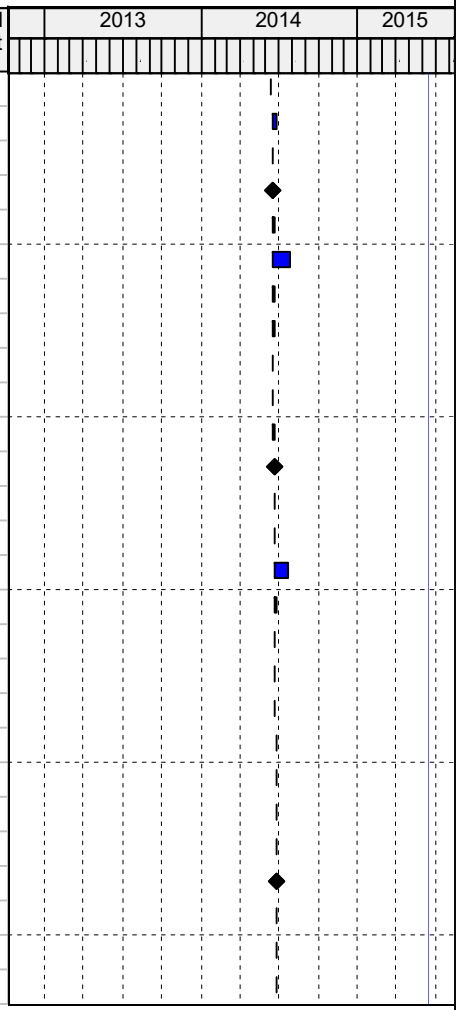



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6012 | Fire Sprinkler Mains | 2 | 0 | 25-Jun-14 A | 22-Jul-14 A | |
| L16-6023 | Inspection of Exterior Framing | 0 | 0 | 25-Jun-14 A | | |
| L03-6024 | Inspections for GWB Cover | 1 | 0 | 27-Jun-14 A | 27-Jun-14 A | |
| L09-6018 | HVAC RI | 3 | 0 | 27-Jun-14 A | 14-Jul-14 A | |
| L09-6221 | Frame Unit Ceilings | 2 | 0 | 27-Jun-14 A | 30-Jun-14 A | |
| L12-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L14-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 27-Jun-14 A | 03-Jul-14 A | |
| L15-6028 | PreRock at Heat Pumps | 2 | 0 | 30-Jun-14 A | 01-Jul-14 A | |
| L16-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 30-Jun-14 A | 30-Jun-14 A | |
| L16-6010 | Frame Walls | 3 | 0 | 01-Jul-14 A | 03-Jul-14 A | |
| L16-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 01-Jul-14 A | 01-Jul-14 A | |
| L15-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 02-Jul-14 A | 02-Jul-14 A | |
| L15-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 03-Jul-14 A | 03-Jul-14 A | |
| L04-6024 | Inspections for GWB Cover | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L10-6018 | HVAC RI | 3 | 0 | 07-Jul-14 A | 21-Jul-14 A | |
| L11-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L15-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L16-6012 | Fire Sprinkler Mains | 2 | 0 | 07-Jul-14 A | 24-Jul-14 A | |
| L16-6020 | Install Hollow Metal Frames | 2 | 0 | 07-Jul-14 A | 08-Jul-14 A | |
| L16-6028 | PreRock at Heat Pumps | 2 | 0 | 07-Jul-14 A | 14-Jul-14 A | |
| L17-6019 | Complete Top Out GWB | 1 | 0 | 07-Jul-14 A | 08-Aug-14 A | |
| L11-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 08-Jul-14 A | 08-Jul-14 A | |
| L15-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 08-Jul-14 A | 04-Aug-14 A | |
| L17-6011 | PreRock Shafts (2 Layers) & Inspect (Part 2) | 4 | 0 | 08-Jul-14 A | 01-Aug-14 A | |
| L10-6221 | Frame Unit Ceilings | 2 | 0 | 09-Jul-14 A | 10-Jul-14 A | |
| L17-6012 | Fire Sprinkler Mains | 2 | 0 | 09-Jul-14 A | 12-Aug-14 A | |
| L05-6024 | Inspections for GWB Cover | 2 | 0 | 10-Jul-14 A | 10-Jul-14 A | |

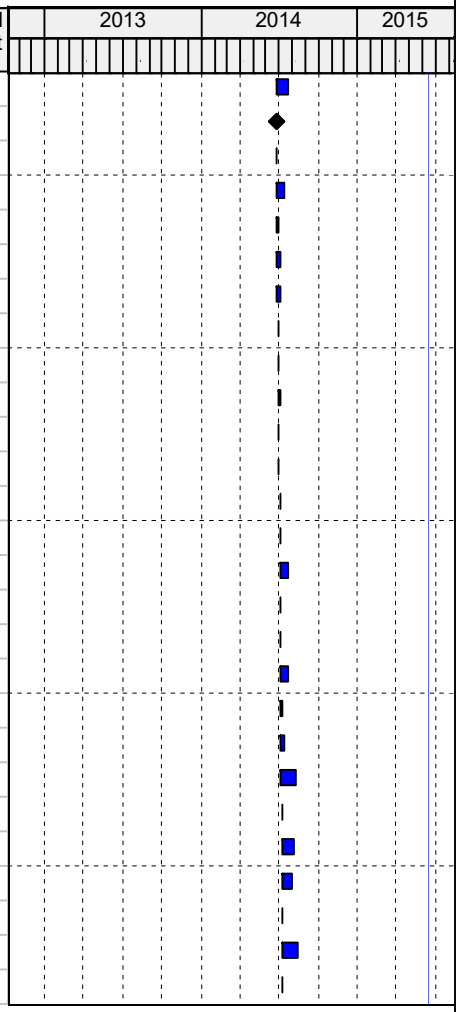


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-6000 | Tape/Finish GWB | 6 | 0 | 11-Jul-14 A | 23-Jul-14 A | |
| L16-6019 | Complete Top Out GWB | 1 | 0 | 14-Jul-14 A | 14-Jul-14 A | |
| L16-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 15-Jul-14 A | 16-Jul-14 A | |
| L15-6018 | HVAC RI | 3 | 0 | 16-Jul-14 A | 18-Jul-14 A | |
| L16-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 16-Jul-14 A | 16-Jul-14 A | |
| L06-6024 | Inspections for GWB Cover | 2 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6018 | HVAC RI | 3 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L16-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 17-Jul-14 A | 17-Jul-14 A | |
| L16-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 21-Jul-14 A | 18-Aug-14 A | |
| L15-6013 | Fire Sprinkler Branch Lines | 1 | 0 | 22-Jul-14 A | 22-Jul-14 A | |
| L03-6000 | Tape/Finish GWB | 6 | 0 | 23-Jul-14 A | 29-Jul-14 A | |
| L11-6018 | HVAC RI | 3 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L15-6221 | Frame Unit Ceilings | 2 | 0 | 23-Jul-14 A | 01-Aug-14 A | |
| L16-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 23-Jul-14 A | 24-Jul-14 A | |
| L17-6020 | Install Hollow Metal Frames | 3 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| L11-6221 | Frame Unit Ceilings | 2 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L12-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L12-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 21-Aug-14 A | |
| L14-6016 | Electrical RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L14-6018 | HVAC RI | 3 | 0 | 28-Jul-14 A | 29-Jul-14 A | |
| L14-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Jul-14 A | 28-Aug-14 A | |
| L16-6014 | Set Tubs & Plumbing RI | 5 | 0 | 28-Jul-14 A | 18-Aug-14 A | |
| L07-6024 | Inspections for GWB Cover | 2 | 0 | 29-Jul-14 A | 30-Jul-14 A | |
| L12-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L14-6221 | Frame Unit Ceilings | 2 | 0 | 30-Jul-14 A | 31-Jul-14 A | |
| L05-6000 | Tape/Finish GWB | 6 | 0 | 31-Jul-14 A | 05-Aug-14 A | |

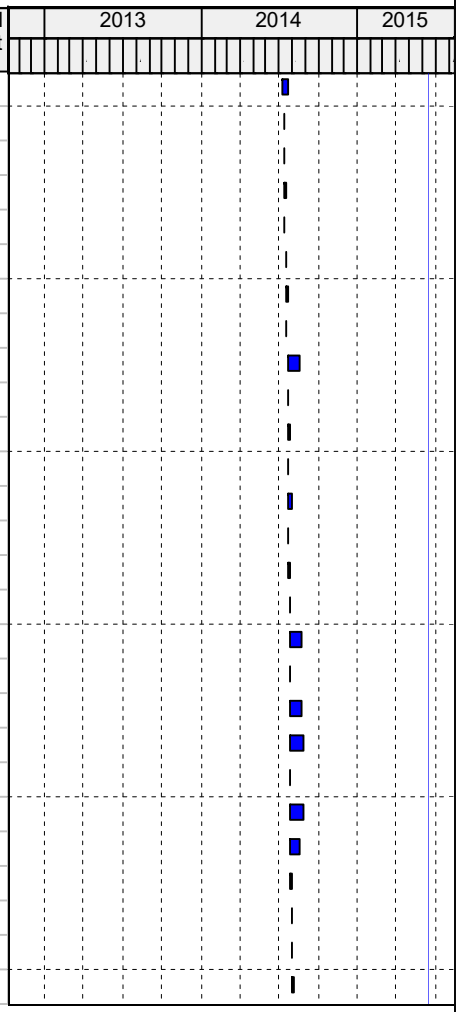


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-6024 | Inspections for GWB Cover | 2 | 0 | 31-Jul-14 A | 31-Jul-14 A | |
| L12-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L14-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L15-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 01-Aug-14 A | 04-Aug-14 A | |
| L06-6000 | Tape/Finish GWB | 4 | 0 | 06-Aug-14 A | 11-Aug-14 A | |
| L09-6024 | Inspections for GWB Cover | 2 | 0 | 06-Aug-14 A | 07-Aug-14 A | |
| L07-6000 | Tape/Finish GWB | 5 | 0 | 07-Aug-14 A | 16-Aug-14 A | |
| L11-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 08-Aug-14 A | 14-Aug-14 A | |
| L17-6014 | Set Tubs & Plumbing RI | 5 | 0 | 08-Aug-14 A | 16-Sep-14 A | |
| L10-6024 | Inspections for GWB Cover | 2 | 0 | 11-Aug-14 A | 12-Aug-14 A | |
| L09-6000 | Tape/Finish GWB | 5 | 0 | 14-Aug-14 A | 19-Aug-14 A | |
| L08-6000 | Tape/Finish GWB | 5 | 0 | 16-Aug-14 A | 21-Aug-14 A | |
| L11-6024 | Inspections for GWB Cover | 2 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L16-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L17-6013 | Fire Sprinkler Branch Lines | 2 | 0 | 18-Aug-14 A | 29-Aug-14 A | |
| L10-6000 | Tape/Finish GWB | 5 | 0 | 19-Aug-14 A | 23-Aug-14 A | |
| L16-6221 | Frame Unit Ceilings | 4 | 0 | 21-Aug-14 A | 26-Aug-14 A | |
| L17-6018 | HVAC RI | 3 | 0 | 21-Aug-14 A | 10-Sep-14 A | |
| L12-6024 | Inspections for GWB Cover | 2 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L15-6016 | Electrical RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L15-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 22-Aug-14 A | 04-Sep-14 A | |
| L11-6000 | Tape/Finish GWB | 5 | 0 | 23-Aug-14 A | 29-Aug-14 A | |
| L17-6221 | Frame Unit Ceilings | 4 | 0 | 26-Aug-14 A | 28-Aug-14 A | |
| L14-6024 | Inspections for GWB Cover | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L16-6016 | Electrical RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L16-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 28-Aug-14 A | 16-Sep-14 A | |
| L12-6000 | Tape/Finish GWB | 5 | 0 | 02-Sep-14 A | 08-Sep-14 A | |

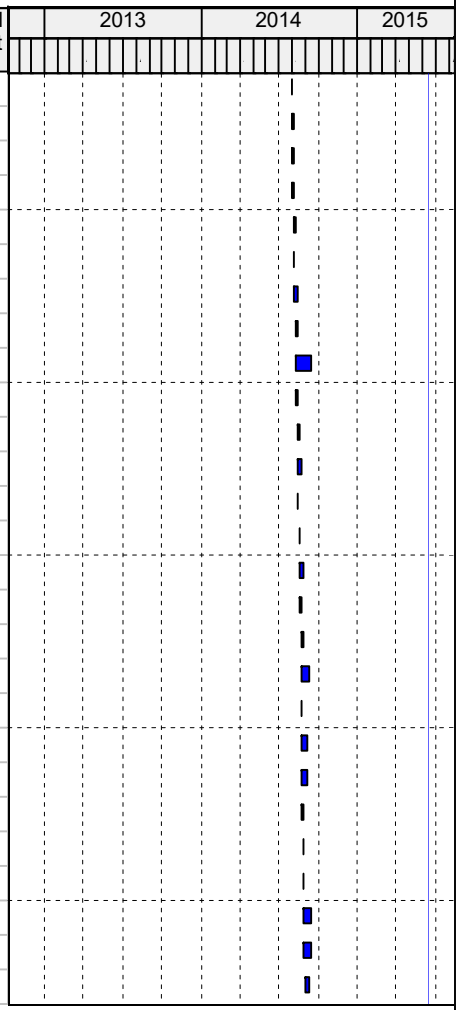



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-6024 | Inspections for GWB Cover | 2 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L14-6000 | Tape/Finish GWB | 5 | 0 | 06-Sep-14 A | 11-Sep-14 A | |
| L15-6000 | Tape/Finish GWB | 4 | 0 | 12-Sep-14 A | 20-Sep-14 A | |
| L17-6016 | Electrical RI | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6022 | Fire Alarm / Elec Specialties RI | 5 | 0 | 16-Sep-14 A | 16-Oct-14 A | |
| L17-6025 | Inst Thermal & VB @ Corners (App to cover 4' of Del | 1 | 0 | 16-Sep-14 A | 16-Sep-14 A | |
| L17-6028 | PreRock at Heat Pumps | 2 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L17-6026 | Inspect Thermal & Vapor Barrier at Heat Pumps | 1 | 0 | 17-Sep-14 A | 17-Sep-14 A | |
| L17-6029 | Inspection of PreRock at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6030 | Tape/Firecaulk at Heat Pumps | 1 | 0 | 23-Sep-14 A | 23-Sep-14 A | |
| L17-6031 | Inspection of Tape/Firecaulk Heat Pumps | 1 | 0 | 24-Sep-14 A | 24-Sep-14 A | |
| L17-6019HP | Install Heat Pumps & Connect to Floor Below | 3 | 0 | 24-Sep-14 A | 27-Sep-14 A | |
| L17-6032 | Install Seismic Bracing at Heat Pumps | 2 | 0 | 25-Sep-14 A | 26-Sep-14 A | |
| L16-6024 | Inspections for GWB Cover | 1 | 0 | 08-Oct-14 A | 09-Oct-14 A | |
| L16-6000 | Tape/Finish GWB | 4 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6024 | Inspections for GWB Cover | 1 | 0 | 17-Oct-14 A | 24-Oct-14 A | |
| L17-6000 | Tape/Finish GWB | 6 | 0 | 30-Oct-14 A | 07-Nov-14 A | |
| **Mechanical Penthouse** | | | | | | |
| PH-6010 | PH - F/P Housekeeping Equip Curbs | 5 | 0 | 11-Jun-14 A | 20-Jun-14 A | |
| PH-6006 | PH - Exterior Wall Framing (including PH roof parapet | 6 | 0 | 12-Jun-14 A | 14-Jul-14 A | |
| PH-6014 | PH - Plumbing/Piping RI | 40 | 0 | 25-Jun-14 A | 05-Nov-14 A | |
| PH-6002 | PH - Layout | 1 | 0 | 25-Jun-14 A | 25-Jun-14 A | |
| PH-6008 | PH - Interior Wall Framing | 3 | 0 | 24-Jul-14 A | 08-Aug-14 A | |
| PH-6020 | PH - H Mtl Frames | 2 | 0 | 08-Aug-14 A | 11-Aug-14 A | |
| PH-6012 | PH - Fire Sprinkler RI | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |
| PH-6018 | PH - HVAC RI | 10 | 0 | 02-Sep-14 A | 12-Sep-14 A | |
| PH-6016 | PH - Electrical RI | 10 | 0 | 23-Sep-14 A | 14-Nov-14 A | |

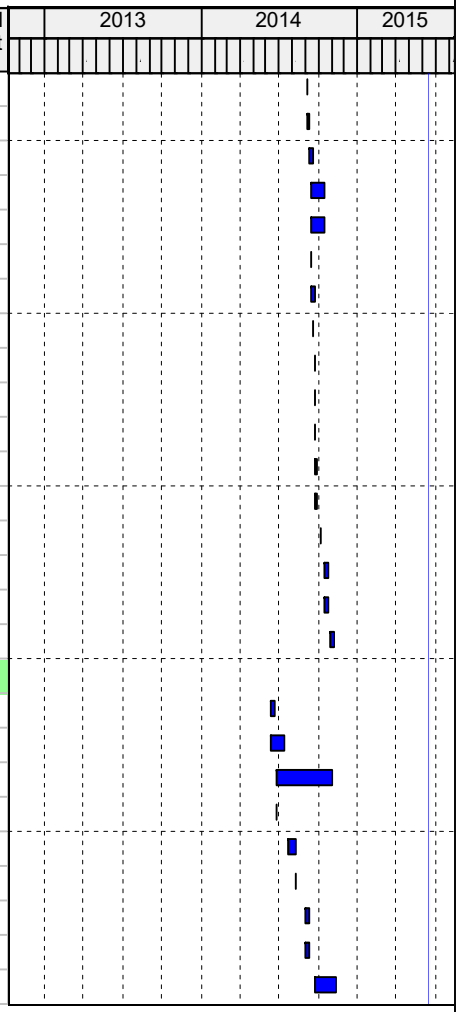


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-6022 | PH - Fire Alarm / Elec Specialties Rl | 10 | 0 | 23-Sep-14 A | 14-Nov-14 A | |
| **Finishes** | | | | | | |
| **Lower Podium - (Levels LL2 / LL1 / 1 / 2)** | | | | | | |
| **Lower Level 4 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL4-8100 | LL4 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| LL4-8102 | LL4 - GWB Hang (incl. screw inspection) | 3 | 0 | 27-Oct-14 A | 10-Dec-14 A | |
| LL4-8114 | LL4 - Striping / Signage (DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL4-8104 | LL4 - Int Painting | 3 | 0 | 22-Dec-14 A | 24-Dec-14 A | |
| LL4-8122 | LL4 - Plumbing Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL4-8108 | Electrical trim & finish | 5 | 0 | 29-Dec-14 A | 16-Feb-15 A | |
| LL4-8112 | LL4 - Fire Sprinkler Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL4-8126 | Install doors & hardware | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL4-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 22-Jan-15 A | 26-Jan-15 A | |
| LL4-8124 | Flooring - VCT | 4 | 0 | 05-Feb-15 A | 06-Feb-15 A | |
| LL4-8110 | HVAC trim | 2 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| LL4-8134 | Final Cleaning - Service Areas | 5 | 0 | 08-Jun-15 A | 12-Jun-15 A | |
| LL4-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 22-Jun-15 | 24-Jun-15 | 7 |
| LL4-8214 | LL4 Floor Complete | 0 | 0 | | 24-Jun-15 | 7 |
| **Lower Level 3 - (Parking)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL3-8100 | LL3 - Insulation | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| LL3-8102 | LL3 - GWB Hang (incl. screw inspection) | 3 | 0 | 27-Oct-14 A | 10-Dec-14 A | |
| LL3-8114 | LL3 - Striping / Signage [DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL3-8104 | LL3 - Int Painting | 3 | 0 | 22-Dec-14 A | 24-Dec-14 A | |
| LL3-8122 | LL3 - Plumbing Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL3-8108 | Electrical trim & finish | 5 | 0 | 29-Dec-14 A | 16-Feb-15 A | |

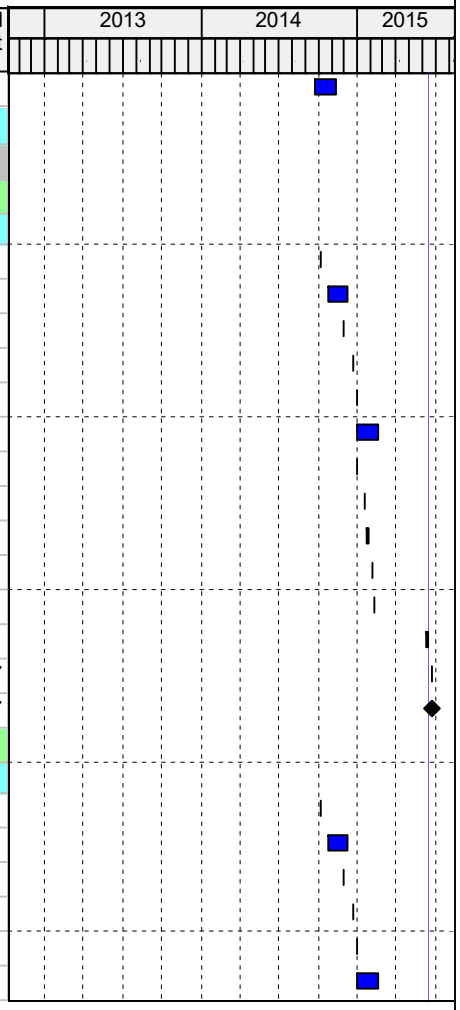



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL3-8112 | LL3 - Fire Sprinkler Trim / Finish | 5 | 0 | 29-Dec-14 A | 29-Dec-14 A | |
| LL3-8126 | Install doors & hardware | 2 | 0 | 19-Jan-15 A | 20-Jan-15 A | |
| LL3-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 22-Jan-15 A | 03-Feb-15 A | |
| LL3-8124 | Flooring - VCT | 4 | 0 | 06-Feb-15 A | 07-Feb-15 A | |
| LL3-8110 | HVAC trim | 2 | 0 | 11-Feb-15 A | 11-Feb-15 A | |
| LL3-8134 | Final Cleaning - Service Areas | 5 | 0 | 08-Jun-15 A | 12-Jun-15 A | |
| LL3-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 22-Jun-15 | 24-Jun-15 | 7 |
| LL3-8214 | LL3 Floor Complete | 0 | 0 | | 24-Jun-15 | 7 |
| **Lower Level 2 - (Parking / Laundry / Elec Rms / Loading Dock)** | | | | | | |
| **Corridors / Common / Public Areas** | | | | | | |
| LL2E-8102 | LL2 - GWB Hang / Tape / Finish @ Electrical Rooms | 8 | 0 | 24-Jun-14 A | 03-Jul-14 A | |
| LL2-8102 | LL2 - GWB Hang / Tape / Finish & Inspection | 6 | 0 | 16-Sep-14 A | 22-Dec-14 A | |
| LL2-8100 | LL2 - Insulation | 5 | 0 | 16-Sep-14 A | 09-Oct-14 A | |
| LL2-8106 | LL2 - Pinned Insulation @ Ceiling | 5 | 0 | 17-Sep-14 A | 27-Oct-14 A | |
| LL2-8138 | LL2 - OH Coiling Grills / Security Door | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| LL2-8104 | LL2 - Int Painting | 5 | 0 | 25-Nov-14 A | 23-Dec-14 A | |
| LL2-8114 | LL2 - Striping / Signage [DELETED, NIC] | 5 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL2-8116 | LL2 - Finish Carpentry / Millwork [DELETED, NONE] | 3 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| LL2-8124 | Flooring - VCT | 4 | 0 | 06-Feb-15 A | 10-Mar-15 A | |
| LL2-8126 | Install doors & hardware | 3 | 0 | 09-Feb-15 A | 16-Feb-15 A | |
| LL2-8122 | Complete MEP trim | 2 | 0 | 08-May-15 A | 08-May-15 A | |
| LL2-8120 | Install bollards at Garage | 2 | 1 | 09-Jun-15 A | 15-Jun-15 | 4 |
| LL2-8134 | Final Cleaning - Service Areas | 5 | 5 | 15-Jun-15 | 19-Jun-15 | 10 |
| LL2-8136 | Chainlink Fencing / Gate @ Recycling at Garage | 3 | 3 | 17-Jun-15 | 19-Jun-15 | 6 |
| LL2-8128 | Entry Gates at Garage | 4 | 4 | 22-Jun-15 | 25-Jun-15 | 2 |
| LL2-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 29-Jun-15 | 01-Jul-15 | 2 |
| **Lower Level 1 - (Mtg Rooms / Excercise / Food Prep)** | | | | | | |

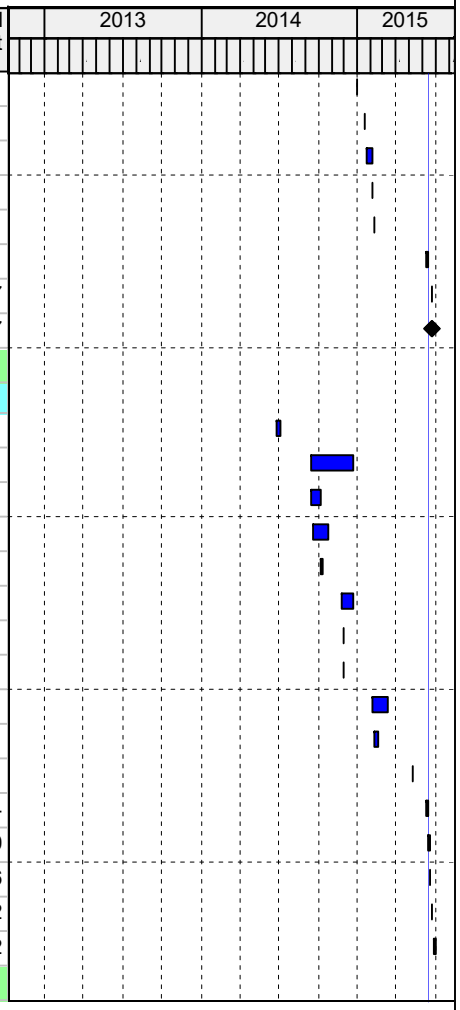



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| **JR Ballrooms / Meeting Rooms / Food Prep / Restrooms** | | | | | | |
| LL1U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 31-Jul-14 A | |
| LL1-Z2U-8102 | Above Ceiling GWB | 5 | 0 | 10-Feb-14 A | 09-May-14 A | |
| LL1-Z3U-8102 | Above Ceiling GWB (At All Areas North of Q-Line) | 5 | 0 | 10-Feb-14 A | 20-Jun-14 A | |
| L1BU-8102 | Above Ceiling GWB [including East Service Corridor] | 5 | 0 | 06-Jun-14 A | 11-Jun-14 A | |
| L1LU-8102 | Above Ceiling GWB | 5 | 0 | 24-Jun-14 A | 13-Oct-14 A | |
| L1KU-8102 | Above Ceiling GWB | 2 | 0 | 26-Jun-14 A | 22-Aug-14 A | |
| LL1-8100 | Insulation | 5 | 0 | 25-Jul-14 A | 29-Jul-14 A | |
| LL1-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 28-Jul-14 A | 06-Aug-14 A | |
| LL1-Z2-8102 | GWB Hang (Walls) & Inspection | 4 | 0 | 11-Aug-14 A | 14-Aug-14 A | |
| LL1-Z2-8100 | Insulation | 3 | 0 | 11-Aug-14 A | 13-Aug-14 A | |
| LL1-8215 | GWB Tape (Walls) | 10 | 0 | 16-Aug-14 A | 07-Nov-14 A | |
| LL1-Z3-8102 | GWB Hang (Walls) & Inspection | 5 | 0 | 15-Sep-14 A | 07-Oct-14 A | |
| LL1-Z3-8100 | Insulation | 5 | 0 | 15-Sep-14 A | 24-Sep-14 A | |
| LL1-Z2-8215 | GWB Tape (Walls/Ceilings) | 7 | 0 | 29-Sep-14 A | 07-Nov-14 A | |
| L1B-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L1K-8100 | Insulation | 5 | 0 | 06-Oct-14 A | 10-Oct-14 A | |
| LL1-Z3-8215 | GWB Tape (Walls & Ceilings) | 7 | 0 | 07-Oct-14 A | 18-Nov-14 A | |
| L1K-8102 | GWB Hang (Walls) & Inspection | 8 | 0 | 09-Oct-14 A | 31-Oct-14 A | |
| L1L-8100 | Insulation | 4 | 0 | 13-Oct-14 A | 16-Oct-14 A | |
| L1B-8102 | GWB Hang (Walls) & Inspection - Main Ballroom N/S/ | 4 | 0 | 16-Oct-14 A | 22-Oct-14 A | |
| L1L-8102 | GWB hang walls (Dining & Lounge) | 4 | 0 | 30-Oct-14 A | 05-Feb-15 A | |
| L1K-8215 | GWB Tape (Walls & Ceilings) | 4 | 0 | 05-Nov-14 A | 18-Nov-14 A | |
| LL1-Z3-8104 | Prime Paint | 4 | 0 | 24-Nov-14 A | 02-Dec-14 A | |
| LL1-8104 | Prime Paint & First Coat Finish Paint | 5 | 0 | 02-Dec-14 A | 12-Dec-14 A | |
| L1K-8106 | Wall coverings - FRP | 8 | 0 | 19-Dec-14 A | 08-Jan-15 A | |
| LL1-Z3-8114 | Ceiling grid & inspection | 4 | 0 | 13-Jan-15 A | 16-Jan-15 A | |

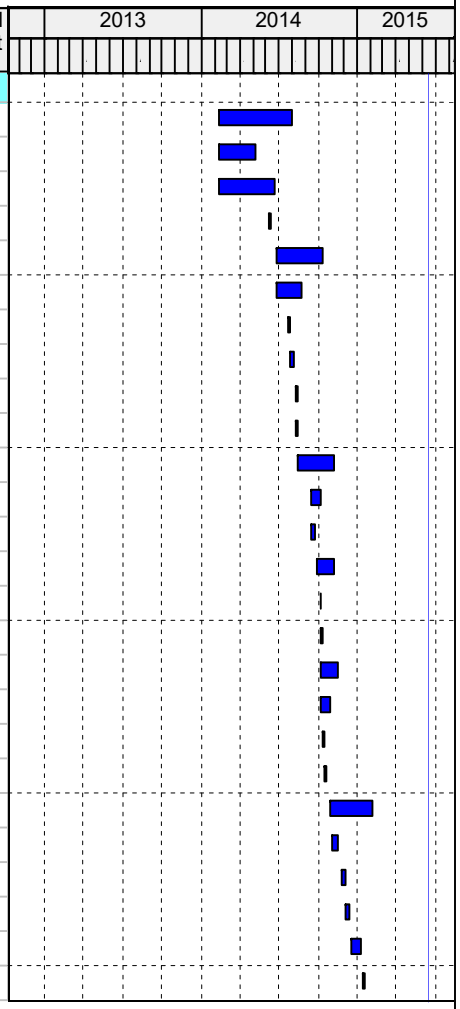


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-8126 | Install doors & hardware | 5 | 0 | 26-Jan-15 A | 03-Feb-15 A | |
| L1L-8215 | GWB hang ceilings (Dining & Lounge) | 5 | 0 | 29-Jan-15 A | 05-Feb-15 A | |
| LL1-8116 | Finish carpentry/millwork | 10 | 0 | 05-Feb-15 A | 02-Mar-15 A | |
| L1K-8114 | Ceiling grid & inspection (east end) | 8 | 0 | 05-Feb-15 A | 13-Mar-15 A | |
| LL1-Z3-8126 | Install doors & hardware | 5 | 0 | 09-Feb-15 A | 12-Feb-15 A | |
| L1K-8124 | Flooring - VCT | 3 | 0 | 10-Feb-15 A | 24-Apr-15 A | |
| LL1-8114 | Ceiling grid & inspection | 4 | 0 | 11-Feb-15 A | 20-Feb-15 A | |
| LL1-8118 | Lighting & electrical drops to grid | 3 | 0 | 12-Feb-15 A | 20-Feb-15 A | |
| LL1-Z2-8104 | Paint, prime at Jr. Ballrooms | 2 | 0 | 12-Feb-15 A | 13-Feb-15 A | |
| L1L-8104 | Paint, prime | 2 | 0 | 13-Feb-15 A | 17-Feb-15 A | |
| LL1-Z2-8126 | Install doors & hardware | 3 | 0 | 16-Feb-15 A | 06-Apr-15 A | |
| LL1-8112 | Fire sprinkler drops to grid | 2 | 0 | 17-Feb-15 A | 20-Feb-15 A | |
| LL1-Z2-8106 | Wall coverings - vinyl at Jr. Ballrooms | 2 | 0 | 18-Feb-15 A | 19-Feb-15 A | |
| LL1-Z2-8114 | Ceiling grid & inspection | 5 | 0 | 18-Feb-15 A | 26-Feb-15 A | |
| L1L-8114 | Install 9-wood ceiling supports - north of Grid K | 3 | 0 | 19-Feb-15 A | 26-Feb-15 A | |
| LL1-Z2-8116 | Finish carpentry/millwork | 10 | 0 | 20-Feb-15 A | 02-Mar-15 A | |
| L1K-8104 | Paint, prime | 2 | 0 | 26-Feb-15 A | 27-Feb-15 A | |
| L1B-8104 | Paint, prime & first coat finish | 3 | 0 | 06-Mar-15 A | 10-Mar-15 A | |
| LL1-Z2-8124 | Flooring - VCT at service corridor | 2 | 0 | 09-Mar-15 A | 11-Mar-15 A | |
| LL1-Z3-8124 | Flooring - epoxy at Food Prep (including prep) | 6 | 0 | 09-Mar-15 A | 13-Mar-15 A | |
| LL1-Z2-8112 | Fire sprinkler drops to grid | 2 | 0 | 16-Mar-15 A | 31-Mar-15 A | |
| LL1-Z2-8118 | Lighting & electrical drops to grid | 3 | 0 | 16-Mar-15 A | 30-Mar-15 A | |
| LL1-Z3-8118 | Lighting & electrical drops at ceiling | 3 | 0 | 16-Mar-15 A | 18-Mar-15 A | |
| LL1-Z3-8112 | Fire sprinkler drops/trim at ceiling | 2 | 0 | 17-Mar-15 A | 28-Apr-15 A | |
| L1L-8140 | Install 9-wood ceiling - north of Grid K | 4 | 0 | 19-Mar-15 A | 31-Mar-15 A | |
| L1L-8116 | Finish carpentry/millwork - north of Grid K | 5 | 0 | 23-Mar-15 A | 27-Mar-15 A | |
| L1L-8126 | Install doors & hardware | 2 | 0 | 23-Mar-15 A | 23-Mar-15 A | |

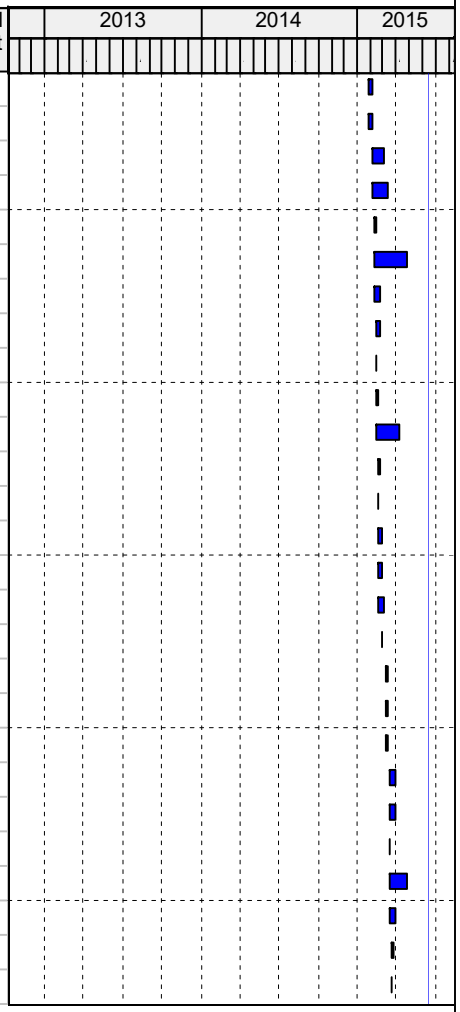


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| LL1-8124 | Flooring - VCT at storage areas, janitorial, mechanica | 3 | 0 | 25-Mar-15 A | 26-Mar-15 A | |
| L1B-8126 | Install doors & hardware at Ballrooms | 2 | 0 | 25-Mar-15 A | 13-Apr-15 A | |
| L1L-8112 | Fire sprinkler trim - north of Grid K | 1 | 0 | 31-Mar-15 A | 31-Mar-15 A | |
| L1K-8116 | Finish carpentry/millwork | 2 | 0 | 06-Apr-15 A | 06-Apr-15 A | |
| L1K-8126 | Install doors & hardware | 3 | 0 | 07-Apr-15 A | 08-Apr-15 A | |
| L1K-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 07-Apr-15 A | 07-Apr-15 A | |
| L1L-8106 | Wall coverings - vinyl | 5 | 0 | 09-Apr-15 A | 27-Apr-15 A | |
| L1B-8116 | Finish carpentry/millwork at Ballrooms | 5 | 0 | 13-Apr-15 A | 17-Apr-15 A | |
| L1L-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 1 | 0 | 13-Apr-15 A | 13-Apr-15 A | |
| L1B-8114 | Ceiling grid & inspection | 3 | 0 | 15-Apr-15 A | 22-Apr-15 A | |
| LL1-Z3-8116 | Install VCT base | 3 | 1 | 29-Apr-15 A | 15-Jun-15 | 10 |
| L1L-8124 | Flooring - wood - north of Grid K | 4 | 0 | 11-May-15 A | 22-May-15 A | |
| L1K-8112 | Fire sprinkler trim | 1 | 0 | 12-May-15 A | 12-May-15 A | |
| LL1-Z2-8140 | Complete acoustical ceiling tile | 2 | 0 | 18-May-15 A | 09-Jun-15 A | |
| L1B-8124 | Flooring - carpet at Ballrooms | 5 | 0 | 20-May-15 A | 28-May-15 A | |
| LL1-Z3-8140 | Complete acoustical ceiling tile | 2 | 0 | 26-May-15 A | 09-Jun-15 A | |
| L1K-8134 | Final Cleaning | 2 | 0 | 26-May-15 A | 27-May-15 A | |
| LL1-8134 | Final Cleaning | 2 | 0 | 01-Jun-15 A | 04-Jun-15 A | |
| LL1-Z2-8134 | Final Cleaning | 2 | 0 | 01-Jun-15 A | 04-Jun-15 A | |
| LL1-Z3-8134 | Final Cleaning | 2 | 0 | 01-Jun-15 A | 04-Jun-15 A | |
| L1B-8164 | Ceiling grid & inspection at Prefunction 2 | 2 | 0 | 05-Jun-15 A | 05-Jun-15 A | |
| L1L-8134 | Final Cleaning - Concierge Lounge | 5 | 5 | 15-Jun-15 | 19-Jun-15 | 5 |
| L1B-8140 | Complete acoustical ceiling tile | 2 | 2 | 17-Jun-15 | 18-Jun-15 | 3 |
| LL1-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 22-Jun-15 | 24-Jun-15 | 7 |
| LL1-Z2-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 22-Jun-15 | 24-Jun-15 | 7 |
| LL1-Z3-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 22-Jun-15 | 24-Jun-15 | 7 |
| L1B-8134 | Final Cleaning - Main Ballroom & Corridors | 5 | 5 | 22-Jun-15 | 26-Jun-15 | 5 |

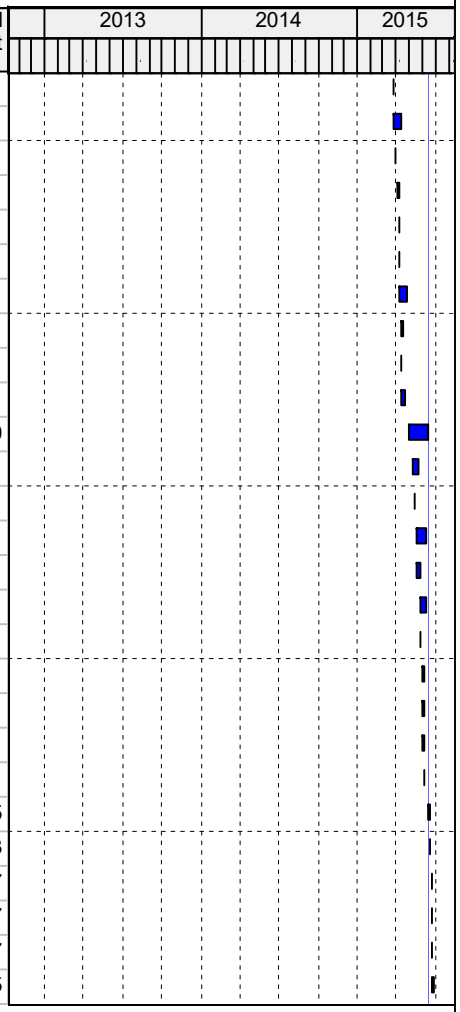



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L1K-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 22-Jun-15 | 24-Jun-15 | 7 |
| L1L-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 24-Jun-15 | 26-Jun-15 | 5 |
| L1B-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 29-Jun-15 | 01-Jul-15 | 2 |
| **Corridors / Common / Public Areas** | | | | | | |
| LL1-8200 | Wall coverings - vinyl | 4 | 0 | 17-Dec-14 A | 19-Jan-15 A | |
| LL1-Z3-8200 | Paint, first coat finish | 4 | 0 | 07-Jan-15 A | 12-Jan-15 A | |
| LL1-Z3-8204 | HVAC drops/trim at ceiling | 2 | 0 | 02-Feb-15 A | 17-Mar-15 A | |
| LL1-8204 | HVAC drops/trim to grid | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| LL1-Z2-8200 | Paint, first coat finish at Jr. Ballrooms | 1 | 0 | 16-Feb-15 A | 16-Feb-15 A | |
| L1L-8200 | Paint, first coat finish | 2 | 0 | 18-Feb-15 A | 18-Feb-15 A | |
| L1K-8200 | Paint, first coat finish | 1 | 0 | 02-Mar-15 A | 02-Mar-15 A | |
| LL1-Z2-8204 | HVAC drops/trim to grid | 2 | 0 | 16-Mar-15 A | 17-Mar-15 A | |
| L1L-8204 | HVAC trim at ceiling - north of Grid K | 1 | 0 | 27-Mar-15 A | 14-Apr-15 A | |
| L1B-8200 | Paint ceiling clouds | 3 | 0 | 02-Apr-15 A | 03-Apr-15 A | |
| L1K-8204 | HVAC drops/trim at ceiling | 1 | 0 | 20-Apr-15 A | 20-Apr-15 A | |
| L1B-8201 | Complete paint final coat & touch-up | 2 | 0 | 07-May-15 A | 08-May-15 A | |
| LL1-8214 | LL1, Zone 1 Complete | 0 | 0 | | 24-Jun-15 | 7 |
| LL1-Z2-8214 | LL1 Zone 2 Complete | 0 | 0 | | 24-Jun-15 | 7 |
| LL1-Z3-8214 | LL1, Zone 3 Complete | 0 | 0 | | 24-Jun-15 | 7 |
| L1K-8214 | L1, Zone 1 Complete | 0 | 0 | | 24-Jun-15 | 7 |
| L1L-8214 | L1, Zone 4 Complete | 0 | 0 | | 26-Jun-15 | 5 |
| L1B-8214 | L1, Zone 2 Complete | 0 | 0 | | 01-Jul-15 | 2 |
| **Level 2 - (Admin / Employee Areas)** | | | | | | |
| **Admin / Employee Areas** | | | | | | |
| L02-8100 | L2 - Insulation - North Half | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L02-8102 | L2 - GWB Hang / Tape / Finish - North Half | 7 | 0 | 23-Oct-14 A | 17-Dec-14 A | |
| L02-8126 | Install doors & hardware at south half | 5 | 0 | 23-Mar-15 A | 15-Apr-15 A | |

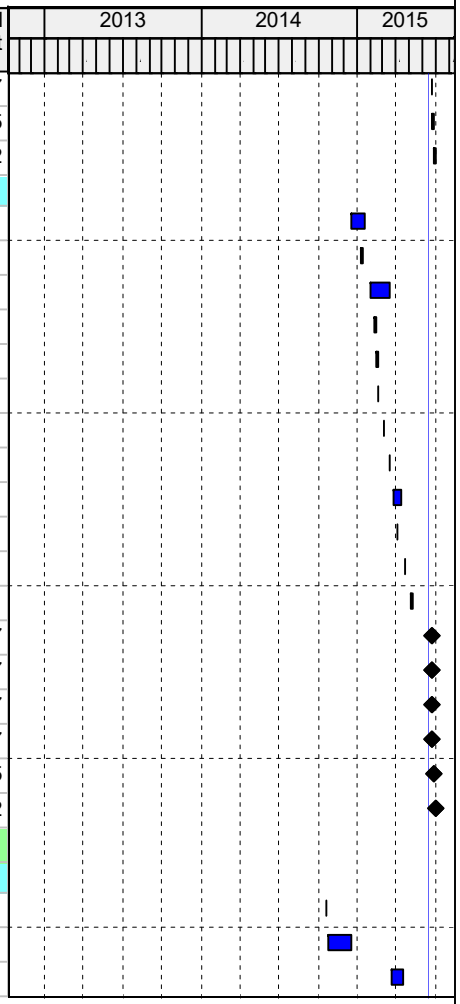


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L02-8112 | Fire sprinkler drops/trim at south half | 2 | 0 | 01-Apr-15 A | 12-May-15 A | |
| L02-8120 | Ceramic tile | 15 | 0 | 02-Apr-15 A | 22-Apr-15 A | |
| L02-8104 | Paint, prime & first coat finish at north half | 2 | 0 | 03-Apr-15 A | 09-Apr-15 A | |
| L02-8106 | Wall coverings - vinyl at south half | 4 | 0 | 07-Apr-15 A | 14-Apr-15 A | |
| L02-8110 | HVAC drops/trim at south half | 2 | 0 | 15-Apr-15 A | 04-May-15 A | |
| L02-8118 | Fire alarm trim (speaker strobe & smoke detector bas | 2 | 0 | 15-Apr-15 A | 16-Apr-15 A | |
| L02-8108 | Complete MEP trim (DELETED) | 2 | 0 | 01-May-15 A | 01-May-15 A | |
| L02-8122 | Plumbing fixtures & trim | 4 | 0 | 13-May-15 A | 27-May-15 A | |
| L02-8124 | Flooring - carpet | 4 | 0 | 19-May-15 A | 28-May-15 A | |
| L02-8116 | Install base | 2 | 0 | 29-May-15 A | 12-Jun-15 A | |
| L02-8136 | Lockers / Benches @ Locker Rooms | 3 | 0 | 01-Jun-15 A | 03-Jun-15 A | |
| L02-8128 | Install bathroom accessories | 3 | 1 | 03-Jun-15 A | 15-Jun-15 | 9 |
| L02-8132 | Owner Punchlist (inspect/distribute/correct) | 3 | 3 | 19-Jun-15 | 23-Jun-15 | 8 |
| L02-8134 | Final Cleaning | 5 | 5 | 22-Jun-15 | 26-Jun-15 | 5 |
| **Corridors** | | | | | | |
| L02-8200 | Complete paint final coat & touch-up (DELETED) | 2 | 0 | 01-May-15 A | 01-May-15 A | |
| L02-8214 | Floor Complete | 0 | 0 | | 26-Jun-15 | 5 |
| **Upper Tower - (Levels 3 thru PH)** | | | | | | |
| **Level 3 - (Guest Rooms / Pool)** | | | | | | |
| **Guest Rooms** | | | | | | |
| L03-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L04-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L05-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L06-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L07-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L08-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L09-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |

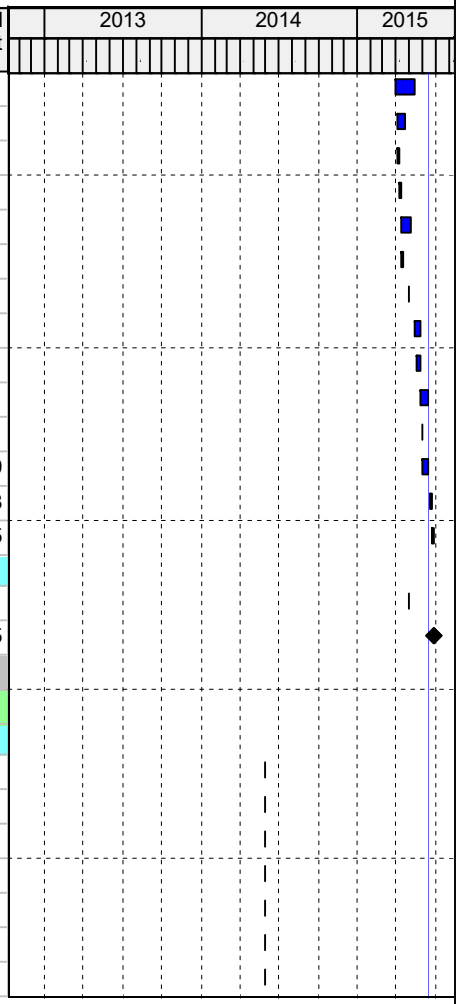



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L11-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L12-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L14-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L15-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L16-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L17-8125 | Ceramic Tile @ Bathrooms [DELETED] | 0 | 0 | 01-Jun-14 A | 01-Jun-14 A | |
| L03-8102S | Stock GWB | 2 | 0 | 27-Jun-14 A | 08-Jul-14 A | |
| L04-8102 | Hang GWB & Inspection | 4 | 0 | 07-Jul-14 A | 16-Jul-14 A | |
| L04-8102S | Stock GWB | 2 | 0 | 07-Jul-14 A | 07-Jul-14 A | |
| L03-8102 | Hang GWB & Inspection | 5 | 0 | 09-Jul-14 A | 22-Jul-14 A | |
| L05-8102S | Stock GWB | 2 | 0 | 10-Jul-14 A | 14-Jul-14 A | |
| L05-8102 | Hang GWB & Inspection | 4 | 0 | 17-Jul-14 A | 23-Jul-14 A | |
| L06-8102S | Stock GWB | 2 | 0 | 17-Jul-14 A | 21-Jul-14 A | |
| L04-8104 | Paint (Prime) | 2 | 0 | 28-Jul-14 A | 05-Aug-14 A | |
| L03-8104 | Paint (Prime) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L03-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 30-Jul-14 A | 04-Aug-14 A | |
| L07-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L08-8102S | Stock GWB | 2 | 0 | 30-Jul-14 A | 30-Jul-14 A | |
| L06-8102 | Hang GWB & Inspection | 5 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L07-8102 | Hang GWB & Inspection | 6 | 0 | 31-Jul-14 A | 06-Aug-14 A | |
| L04-8105 | Paint (First Coat & Ceilings) | 5 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L05-8104 | Paint (Prime) | 2 | 0 | 06-Aug-14 A | 08-Aug-14 A | |
| L09-8102S | Stock GWB | 2 | 0 | 06-Aug-14 A | 06-Aug-14 A | |
| L05-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 07-Aug-14 A | 11-Aug-14 A | |
| L09-8102 | Hang GWB & Inspection | 5 | 0 | 07-Aug-14 A | 13-Aug-14 A | |
| L08-8102 | Hang GWB & Inspection | 6 | 0 | 11-Aug-14 A | 15-Aug-14 A | |

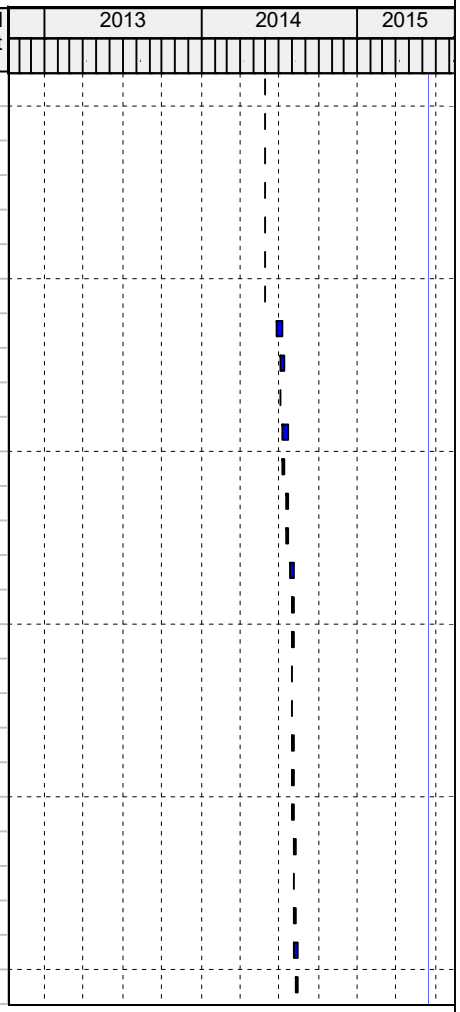



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8104 | Paint (Prime) | 2 | 0 | 12-Aug-14 A | 13-Aug-14 A | |
| L10-8102S | Stock GWB | 1 | 0 | 12-Aug-14 A | 12-Aug-14 A | |
| L10-8102 | Hang GWB & Inspection | 4 | 0 | 13-Aug-14 A | 18-Aug-14 A | |
| L06-8105 | Paint (First Coat & Ceilings) | 2 | 0 | 14-Aug-14 A | 18-Aug-14 A | |
| L11-8102S | Stock GWB | 1 | 0 | 16-Aug-14 A | 16-Aug-14 A | |
| L07-8104 | Paint (Prime) | 2 | 0 | 18-Aug-14 A | 19-Aug-14 A | |
| L11-8102 | Hang GWB & Inspection | 4 | 0 | 18-Aug-14 A | 22-Aug-14 A | |
| L07-8105 | Paint (First Coat & Ceilings) | 4 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L09-8104 | Paint (Prime) | 2 | 0 | 20-Aug-14 A | 28-Aug-14 A | |
| L08-8104 | Paint (Prime) | 2 | 0 | 22-Aug-14 A | 25-Aug-14 A | |
| L12-8102 | Hang GWB & Inspection | 4 | 0 | 22-Aug-14 A | 30-Aug-14 A | |
| L12-8102S | Stock GWB | 1 | 0 | 22-Aug-14 A | 22-Aug-14 A | |
| L03-8108 | Elec Trim / Finish | 4 | 0 | 25-Aug-14 A | 04-Sep-14 A | |
| L08-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 26-Aug-14 A | 29-Aug-14 A | |
| L03-8118 | Fire Alarm Trim / Finish | 3 | 0 | 27-Aug-14 A | 29-Sep-14 A | |
| L14-8102S | Stock GWB | 1 | 0 | 28-Aug-14 A | 28-Aug-14 A | |
| L09-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 29-Aug-14 A | 09-Sep-14 A | |
| L14-8102 | Hang GWB & Inspection | 5 | 0 | 29-Aug-14 A | 05-Sep-14 A | |
| L03-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 02-Sep-14 A | 05-Sep-14 A | |
| L04-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 04-Sep-14 A | 09-Sep-14 A | |
| L10-8104 | Paint (Prime) | 2 | 0 | 04-Sep-14 A | 05-Sep-14 A | |
| L15-8102S | Stock GWB | 1 | 0 | 05-Sep-14 A | 05-Sep-14 A | |
| L15-8102 | Hang GWB & Inspection | 5 | 0 | 06-Sep-14 A | 12-Sep-14 A | |
| L03-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 15-Sep-14 A | |
| L04-8108 | Elec Trim / Finish | 4 | 0 | 08-Sep-14 A | 16-Sep-14 A | |
| L04-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 08-Sep-14 A | 11-Sep-14 A | |
| L05-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 08-Sep-14 A | 12-Sep-14 A | |

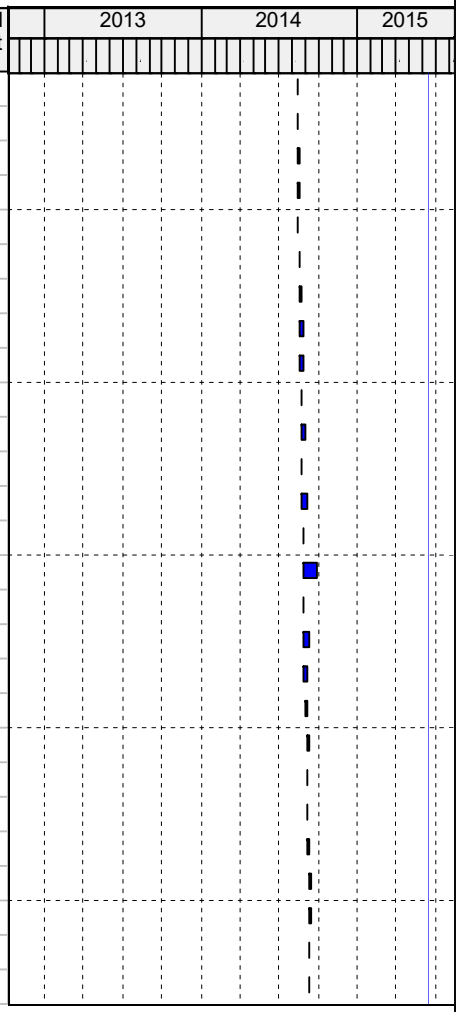


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 08-Sep-14 A | 12-Sep-14 A | |
| L11-8104 | Paint (Prime) | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L05-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 09-Sep-14 A | 09-Sep-14 A | |
| L04-8116 | Install Base at Guestrooms | 5 | 0 | 10-Sep-14 A | 17-Sep-14 A | |
| L11-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 10-Sep-14 A | 22-Sep-14 A | |
| L03-8116 | Install Base at Guestrooms | 5 | 0 | 12-Sep-14 A | 16-Sep-14 A | |
| L12-8104 | Paint (Prime) | 2 | 0 | 12-Sep-14 A | 17-Sep-14 A | |
| L05-8116 | Install Base at Guestrooms | 5 | 0 | 16-Sep-14 A | 24-Sep-14 A | |
| L06-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 16-Sep-14 A | 22-Sep-14 A | |
| L05-8108 | Elec Trim / Finish | 4 | 0 | 17-Sep-14 A | 22-Sep-14 A | |
| L07-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 17-Sep-14 A | 23-Sep-14 A | |
| L12-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 17-Sep-14 A | 06-Oct-14 A | |
| L06-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L07-8116 | Install Base at Guestrooms | 5 | 0 | 22-Sep-14 A | 26-Sep-14 A | |
| L14-8104 | Paint (Prime) | 2 | 0 | 22-Sep-14 A | 23-Sep-14 A | |
| L06-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L06-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8108 | Elec Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L07-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L08-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 24-Sep-14 A | 29-Sep-14 A | |
| L14-8105 | Paint (First Coat & Ceilings) | 3 | 0 | 24-Sep-14 A | 06-Oct-14 A | |
| L15-8104 | Paint (Prime) | 2 | 0 | 24-Sep-14 A | 25-Sep-14 A | |
| L03-8110 | HVAC Grilles & Registers | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L03-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Sep-14 A | 13-Oct-14 A | |
| L04-8118 | Fire Alarm Trim / Finish | 3 | 0 | 29-Sep-14 A | 01-Oct-14 A | |
| L10-8112 | Fire Sprinkler Trim / Finish | 4 | 0 | 29-Sep-14 A | 01-Oct-14 A | |

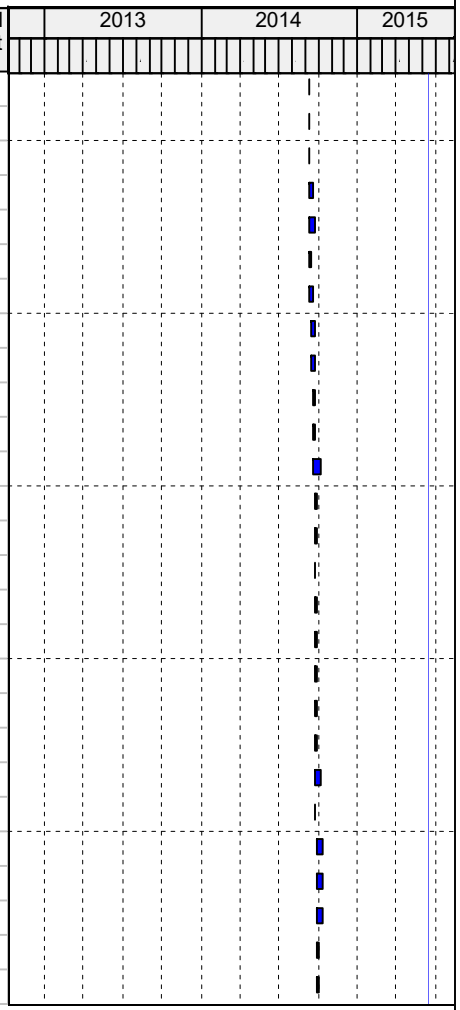


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L08-8124 | Guestroom/Bathroom Flooring | 5 | 0 | 30-Sep-14 A | 06-Oct-14 A | |
| L03-8126 | Install Doors | 3 | 0 | 01-Oct-14 A | 07-Oct-14 A | |
| L03-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 01-Oct-14 A | 28-Oct-14 A | |
| L04-8126 | Install Doors | 3 | 0 | 02-Oct-14 A | 09-Oct-14 A | |
| L08-8116 | Install Base at Guestrooms | 5 | 0 | 02-Oct-14 A | 08-Oct-14 A | |
| L04-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8110 | HVAC Grilles & Registers | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8118 | Fire Alarm Trim / Finish | 3 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L08-8108 | Elec Trim / Finish | 4 | 0 | 06-Oct-14 A | 08-Oct-14 A | |
| L15-8105 | Paint - First Coast & Ceilings | 3 | 0 | 06-Oct-14 A | 13-Oct-14 A | |
| L05-8126 | Install Doors | 3 | 0 | 08-Oct-14 A | 10-Oct-14 A | |
| L09-8116 | Install Base and Door Thresholds | 5 | 0 | 08-Oct-14 A | 15-Oct-14 A | |
| L09-8124 | Install Flooring | 5 | 0 | 08-Oct-14 A | 14-Oct-14 A | |
| L16-8102S | Stock GWB | 1 | 0 | 08-Oct-14 A | 08-Oct-14 A | |
| L09-8112 | Fire Sprinkler Trim | 2 | 0 | 09-Oct-14 A | 10-Oct-14 A | |
| L16-8102 | Hang GWB & Inspection | 4 | 0 | 10-Oct-14 A | 17-Oct-14 A | |
| L06-8118 | Fire Alarm Trim / Finish | 3 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L09-8108 | Lighting and Electrical Trim | 3 | 0 | 13-Oct-14 A | 15-Oct-14 A | |
| L10-8124 | Install Flooring | 5 | 0 | 13-Oct-14 A | 16-Oct-14 A | |
| L11-8112 | Fire Sprinkler Trim | 2 | 0 | 13-Oct-14 A | 14-Oct-14 A | |
| L03-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 14-Oct-14 A | 04-Nov-14 A | |
| L06-8110 | HVAC Grilles & Registers | 2 | 0 | 14-Oct-14 A | 21-Oct-14 A | |
| L06-8126 | Install Doors | 2 | 0 | 14-Oct-14 A | 20-Oct-14 A | |
| L07-8118 | Fire Alarm Trim / Finish | 3 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L12-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L14-8112 | Fire Sprinkler Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L08-8118 | Fire Alarm Trim / Finish | 3 | 0 | 15-Oct-14 A | 16-Oct-14 A | |

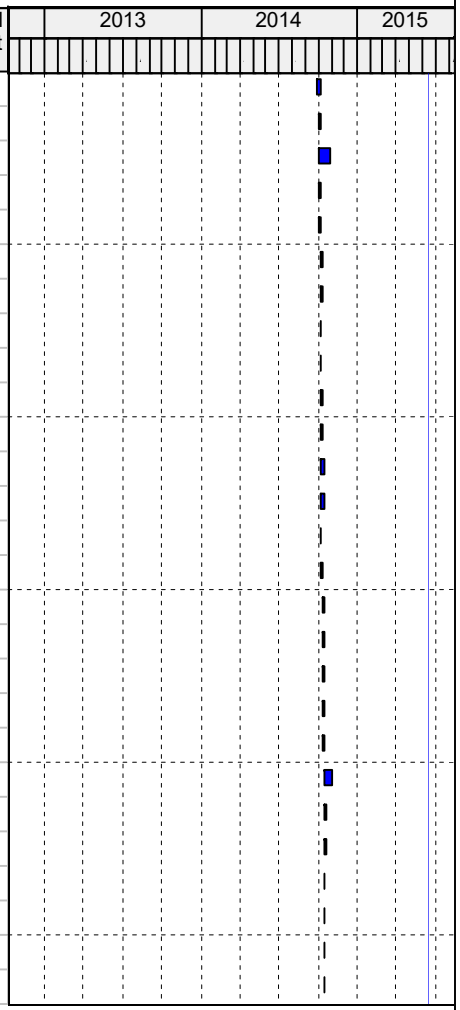



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L10-8116 | Install Base and Door Thresholds | 5 | 0 | 15-Oct-14 A | 23-Oct-14 A | |
| L15-8112 | Fire Sprinkler Trim | 2 | 0 | 15-Oct-14 A | 16-Oct-14 A | |
| L04-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 16-Oct-14 A | 11-Nov-14 A | |
| L11-8124 | Install Flooring | 5 | 0 | 16-Oct-14 A | 22-Oct-14 A | |
| L17-8102S | Stock GWB | 1 | 0 | 17-Oct-14 A | 17-Oct-14 A | |
| L07-8126 | Install Doors | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |
| L09-8118 | Fire Alarm Trim | 2 | 0 | 20-Oct-14 A | 20-Oct-14 A | |
| L05-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 21-Oct-14 A | 14-Nov-14 A | |
| L08-8126 | Install Doors | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L10-8118 | Fire Alarm Trim | 2 | 0 | 21-Oct-14 A | 21-Oct-14 A | |
| L09-8126 | Install Doors | 2 | 0 | 22-Oct-14 A | 23-Oct-14 A | |
| L11-8118 | Fire Alarm Trim | 2 | 0 | 22-Oct-14 A | 22-Oct-14 A | |
| L06-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 23-Oct-14 A | 19-Nov-14 A | |
| L10-8126 | Install Doors | 2 | 0 | 23-Oct-14 A | 27-Oct-14 A | |
| L12-8124 | Install Flooring | 5 | 0 | 23-Oct-14 A | 29-Oct-14 A | |
| L12-8118 | Fire Alarm Trim | 2 | 0 | 23-Oct-14 A | 23-Oct-14 A | |
| L11-8116 | Install Base and Door Thresholds | 5 | 0 | 24-Oct-14 A | 26-Nov-14 A | |
| L07-8110 | HVAC Grilles & Registers | 2 | 0 | 27-Oct-14 A | 28-Oct-14 A | |
| L10-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |
| L11-8108 | Lighting and Electrical Trim | 3 | 0 | 27-Oct-14 A | 29-Oct-14 A | |
| L17-8102 | Hang GWB & Inspection | 4 | 0 | 27-Oct-14 A | 03-Nov-14 A | |
| L07-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 28-Oct-14 A | 26-Nov-14 A | |
| L08-8120 | Bathrooms - Install Countertops | 3 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L11-8126 | Install Doors | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |
| L12-8108 | Lighting and Electrical Trim | 3 | 0 | 28-Oct-14 A | 30-Oct-14 A | |
| L12-8116 | Install Base and Door Thresholds | 5 | 0 | 28-Oct-14 A | 03-Dec-14 A | |
| L14-8118 | Fire Alarm Trim | 2 | 0 | 28-Oct-14 A | 29-Oct-14 A | |

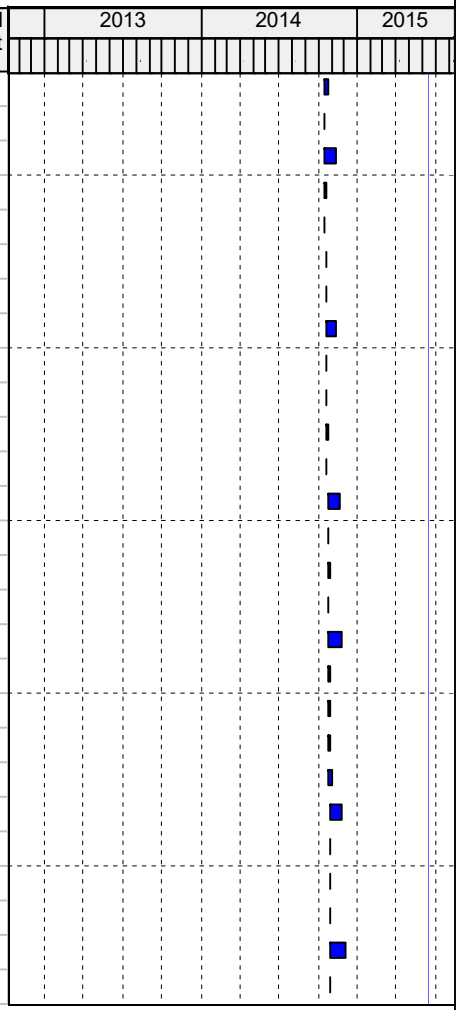



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L05-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Oct-14 A | 31-Oct-14 A | |
| L06-8120 | Bathrooms - Install Countertops | 3 | 0 | 29-Oct-14 A | 31-Oct-14 A | |
| L12-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L14-8108 | Lighting and Electrical Trim | 3 | 0 | 29-Oct-14 A | 03-Nov-14 A | |
| L14-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8126 | Install Doors | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L15-8118 | Fire Alarm Trim | 2 | 0 | 29-Oct-14 A | 30-Oct-14 A | |
| L04-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 30-Oct-14 A | 04-Nov-14 A | |
| L07-8120 | Bathrooms - Install Countertops | 3 | 0 | 03-Nov-14 A | 05-Nov-14 A | |
| L08-8110 | HVAC Grilles & Registers | 2 | 0 | 03-Nov-14 A | 04-Nov-14 A | |
| L09-8120 | Bathrooms - Install Countertops | 3 | 0 | 03-Nov-14 A | 05-Nov-14 A | |
| L10-8120 | Bathrooms - Install Countertops | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| L15-8108 | Lighting and Electrical Trim | 3 | 0 | 04-Nov-14 A | 06-Nov-14 A | |
| L11-8120 | Bathrooms - Install Countertops | 3 | 0 | 05-Nov-14 A | 07-Nov-14 A | |
| L16-8104 | Paint - Prime | 2 | 0 | 05-Nov-14 A | 06-Nov-14 A | |
| L05-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 07-Nov-14 A | 12-Nov-14 A | |
| L16-8105 | Paint - First Coat & Ceilings | 3 | 0 | 07-Nov-14 A | 11-Nov-14 A | |
| L12-8120 | Bathrooms - Install Countertops | 3 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L14-8124 | Install Flooring | 5 | 0 | 10-Nov-14 A | 14-Nov-14 A | |
| L06-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 13-Nov-14 A | 17-Nov-14 A | |
| L15-8124 | Install Flooring | 5 | 0 | 17-Nov-14 A | 25-Nov-14 A | |
| L17-8104 | Paint - Prime | 2 | 0 | 17-Nov-14 A | 18-Nov-14 A | |
| L14-8116 | Install Base and Door Thresholds | 5 | 0 | 18-Nov-14 A | 08-Dec-14 A | |
| L16-8126 | Install Doors | 2 | 0 | 18-Nov-14 A | 19-Nov-14 A | |
| L07-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 19-Nov-14 A | 25-Nov-14 A | |
| L15-8116 | Install Base and Door Thresholds | 5 | 0 | 20-Nov-14 A | 08-Dec-14 A | |
| L03-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |

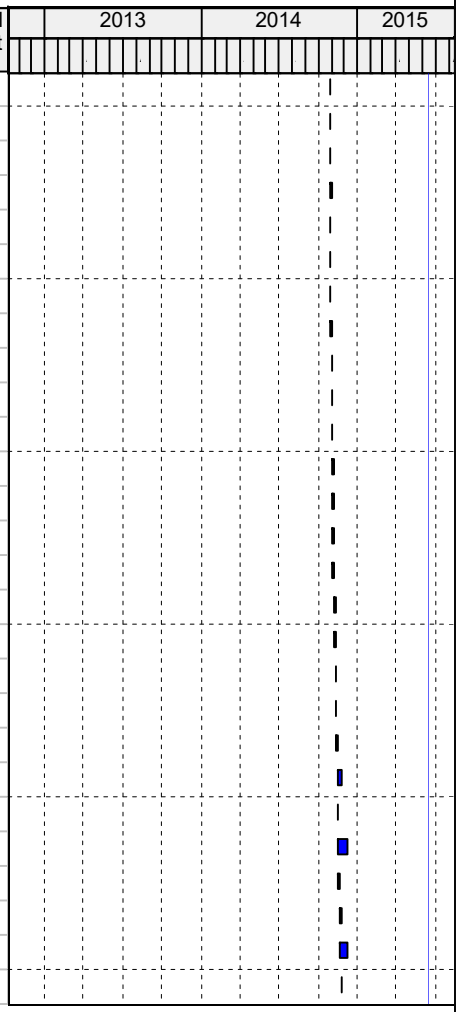



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L04-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L05-8107 | Paint Final Coat | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L08-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 24-Nov-14 A | 01-Dec-14 A | |
| L17-8105 | Paint - First Coat & Ceilings | 3 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| L16-8124 | Install Flooring | 5 | 0 | 25-Nov-14 A | 03-Dec-14 A | |
| L16-8112 | Fire Sprinkler Trim | 2 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| L16-8118 | Fire Alarm Trim | 2 | 0 | 26-Nov-14 A | 01-Dec-14 A | |
| L06-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L07-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L08-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 01-Dec-14 A | 08-Dec-14 A | |
| L08-8107 | Paint Final Coat | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L09-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 01-Dec-14 A | 10-Dec-14 A | |
| L16-8108 | Lighting and Electrical Trim | 3 | 0 | 01-Dec-14 A | 03-Dec-14 A | |
| L17-8126 | Install Doors | 2 | 0 | 01-Dec-14 A | 02-Dec-14 A | |
| L16-8116 | Install Base and Door Thresholds | 5 | 0 | 02-Dec-14 A | 15-Dec-14 A | |
| L17-8112 | Fire Sprinkler Trim | 2 | 0 | 02-Dec-14 A | 02-Dec-14 A | |
| L09-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 03-Dec-14 A | 08-Dec-14 A | |
| L09-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L10-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L11-8107 | Paint Final Coat | 3 | 0 | 03-Dec-14 A | 05-Dec-14 A | |
| L17-8118 | Fire Alarm Trim | 2 | 0 | 03-Dec-14 A | 03-Dec-14 A | |
| L12-8107 | Paint Final Coat | 3 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L14-8120 | Bathrooms - Install Countertops | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L17-8108 | Lighting and Electrical Trim | 3 | 0 | 08-Dec-14 A | 09-Dec-14 A | |
| L10-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 09-Dec-14 A | 11-Dec-14 A | |
| L15-8120 | Bathrooms - Install Countertops | 3 | 0 | 09-Dec-14 A | 10-Dec-14 A | |
| L10-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 10-Dec-14 A | 16-Dec-14 A | |

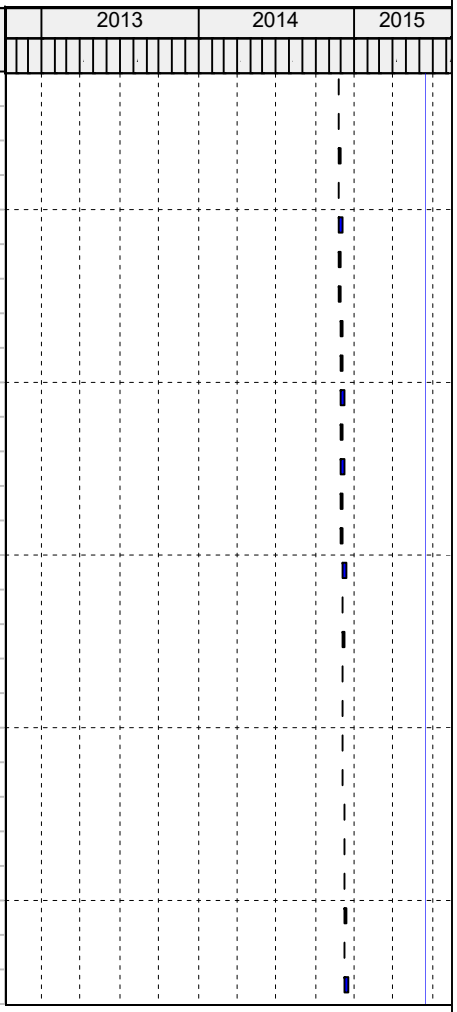



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 10-Dec-14 A | 24-Dec-14 A | |
| L04-8132 | Contractor Punchlist (inspect/distribute/correct/back-pl | 7 | 0 | 11-Dec-14 A | 05-Feb-15 A | |
| L04-8134 | Final Clean @ Guestrooms | 1 | 0 | 11-Dec-14 A | 11-Dec-14 A | |
| L05-8132 | Contractor Punchlist (inspect/distribute/correct/back-pl | 7 | 0 | 12-Dec-14 A | 10-Feb-15 A | |
| L05-8134 | Final Clean @ Guestrooms | 1 | 0 | 12-Dec-14 A | 12-Dec-14 A | |
| L11-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 12-Dec-14 A | 17-Dec-14 A | |
| L06-8134 | Final Clean @ Guestrooms | 5 | 0 | 13-Dec-14 A | 13-Dec-14 A | |
| L12-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 15-Dec-14 A | 18-Dec-14 A | |
| L17-8124 | Install Flooring | 5 | 0 | 15-Dec-14 A | 18-Dec-14 A | |
| L17-8116 | Install Base and Door Thresholds | 5 | 0 | 18-Dec-14 A | 30-Dec-14 A | |
| L12-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| L14-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 22-Dec-14 A | 29-Dec-14 A | |
| L15-8128 | Bathrooms - Install Shower/Tub Surrounds | 4 | 0 | 29-Dec-14 A | 05-Jan-15 A | |
| L16-8120 | Bathrooms - Install countertops | 3 | 0 | 29-Dec-14 A | 09-Jan-15 A | |
| L14-8122 | Bathrooms - Plumbing Fixtures & Trim | 4 | 0 | 30-Dec-14 A | 05-Jan-15 A | |
| L15-8122 | Bathrooms - Plumbing fixtures & trim | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L16-8128 | Bathrooms - Install shower/tub surrounds | 4 | 0 | 05-Jan-15 A | 09-Jan-15 A | |
| L16-8122 | Bathrooms - Plumbing fixtures & trim | 3 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L17-8128 | Bathrooms - Install shower/tub surrounds | 4 | 0 | 12-Jan-15 A | 15-Jan-15 A | |
| L09-8110 | HVAC grilles & registers | 2 | 0 | 14-Jan-15 A | 19-Jan-15 A | |
| L11-8110 | HVAC grilles & registers | 2 | 0 | 21-Jan-15 A | 28-Jan-15 A | |
| L12-8110 | HVAC grilles & registers | 2 | 0 | 21-Jan-15 A | 28-Jan-15 A | |
| L14-8110 | HVAC grilles & registers | 2 | 0 | 21-Jan-15 A | 02-Feb-15 A | |
| L10-8110 | HVAC grilles & registers | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L15-8110 | HVAC grilles & registers | 2 | 0 | 03-Feb-15 A | 16-Feb-15 A | |
| L16-8110 | HVAC grilles & registers | 2 | 0 | 03-Feb-15 A | 23-Feb-15 A | |
| L17-8122 | Bathrooms - Plumbing fixtures & trim | 3 | 0 | 03-Feb-15 A | 06-May-15 A | |

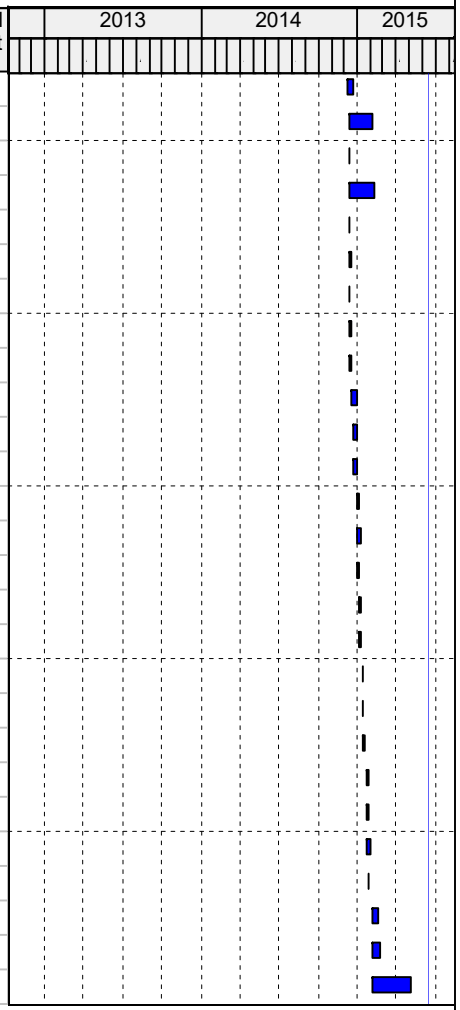


Actual Work | Critical Remai... | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L17-8120 | Bathrooms - Install countertops | 3 | 0 | 03-Feb-15 A | 24-Apr-15 A | |
| L06-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 04-Feb-15 A | 12-Feb-15 A | |
| L07-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 06-Feb-15 A | 20-Feb-15 A | |
| L14-8107 | Paint, final coat & touch-up | 3 | 0 | 09-Feb-15 A | 11-Feb-15 A | |
| L17-8110 | HVAC grilles & registers | 2 | 0 | 09-Feb-15 A | 31-Mar-15 A | |
| L08-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 10-Feb-15 A | 07-Mar-15 A | |
| L09-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 12-Feb-15 A | 06-Mar-15 A | |
| L15-8107 | Paint, final coat & touch-up | 3 | 0 | 16-Feb-15 A | 18-Feb-15 A | |
| L10-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 18-Feb-15 A | 13-Mar-15 A | |
| L11-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 20-Feb-15 A | 20-Mar-15 A | |
| L16-8107 | Paint, final coat & touch-up | 3 | 0 | 24-Feb-15 A | 26-Feb-15 A | |
| L12-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 25-Feb-15 A | 25-Mar-15 A | |
| L14-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 26-Feb-15 A | 27-Mar-15 A | |
| L03-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L04-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L05-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L06-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L07-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L08-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L09-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L10-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L11-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L12-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 04-Mar-15 A | 04-Mar-15 A | |
| L14-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L15-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L16-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 05-Mar-15 A | 05-Mar-15 A | |
| L17-8109 | Acoustical ceiling tile at corridors | 1 | 0 | 05-Mar-15 A | 05-Mar-15 A | |

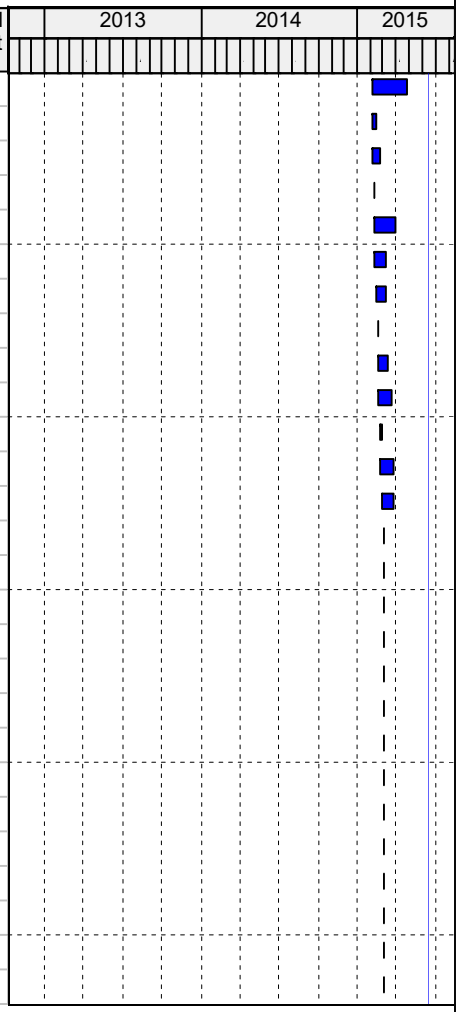



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L15-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 06-Mar-15 A | 06-Apr-15 A | |
| L16-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 7 | 0 | 10-Mar-15 A | 08-Apr-15 A | |
| L17-8107 | Paint, final coat & touch-up | 2 | 0 | 25-Mar-15 A | 26-Mar-15 A | |
| L03-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 0 | 13-Apr-15 A | 17-Apr-15 A | |
| L17-8132 | Contractor Punchlist (inspect/distribute/correct/back-p | 5 | 0 | 04-May-15 A | 07-May-15 A | |
| **Pool Area** | | | | | | |
| L03-8216 | Install pool tile, coping and depth markers | 5 | 5 | 26-Jun-15 | 02-Jul-15 | 0 |
| **Corridors / Common / Public Areas** | | | | | | |
| L03-8200 | Vinyl Wall Coverings | 3 | 0 | 01-Aug-14 A | 05-Aug-14 A | |
| L04-8200 | Vinyl Wall Coverings | 5 | 0 | 06-Aug-14 A | 12-Aug-14 A | |
| L05-8200 | Vinyl Wall Coverings | 5 | 0 | 12-Aug-14 A | 22-Sep-14 A | |
| L03-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 08-Sep-14 A | 09-Sep-14 A | |
| L06-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L07-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 10-Sep-14 A | 16-Sep-14 A | |
| L08-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 11-Sep-14 A | 19-Sep-14 A | |
| L04-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 15-Sep-14 A | 16-Sep-14 A | |
| L05-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 17-Sep-14 A | 18-Sep-14 A | |
| L06-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L07-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 26-Sep-14 A | 29-Sep-14 A | |
| L09-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 07-Oct-14 A | |
| L10-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 08-Oct-14 A | |
| L11-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 5 | 0 | 29-Sep-14 A | 10-Oct-14 A | |
| L08-8202 | Elec Trim / Finish @ Corridors & Inspection | 2 | 0 | 06-Oct-14 A | 07-Oct-14 A | |
| L12-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 13-Oct-14 A | 17-Oct-14 A | |
| L09-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 14-Oct-14 A | 15-Oct-14 A | |
| L14-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 16-Oct-14 A | 27-Oct-14 A | |
| L10-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 20-Oct-14 A | 21-Oct-14 A | |

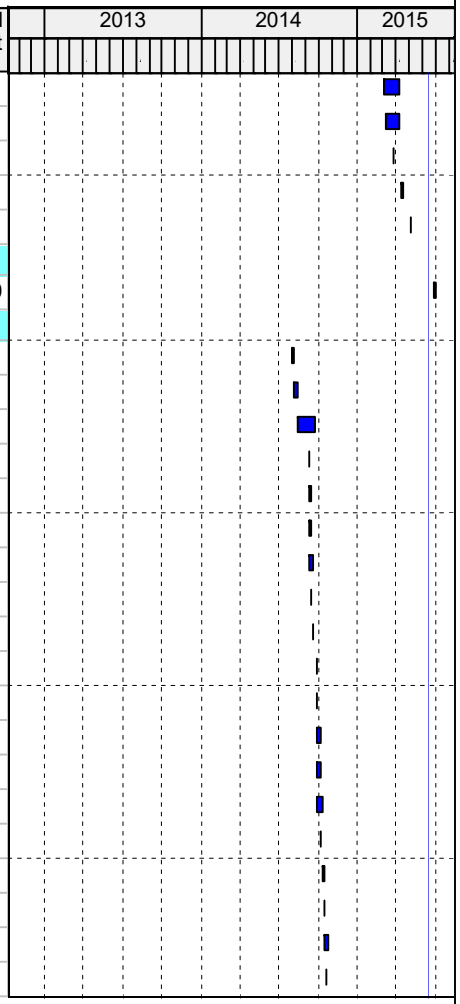



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L11-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 21-Oct-14 A | 22-Oct-14 A | |
| L15-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 22-Oct-14 A | 29-Oct-14 A | |
| L12-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 03-Nov-14 A | 04-Nov-14 A | |
| L14-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 04-Nov-14 A | 05-Nov-14 A | |
| L15-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 05-Nov-14 A | 06-Nov-14 A | |
| L16-8200 | Vinyl Wall Coverings - Window Niches & Outside Bath | 4 | 0 | 14-Nov-14 A | 20-Nov-14 A | |
| L16-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 18-Nov-14 A | 18-Nov-14 A | |
| L17-8202 | Corridors - Lighting and Electrical Trim | 2 | 0 | 08-Dec-14 A | 10-Dec-14 A | |
| L17-8200 | Wall coverings - vinyl at window niches & outside batl | 4 | 0 | 15-Dec-14 A | 24-Mar-15 A | |
| L04-8206 | Flooring - carpet at corridors | 2 | 0 | 14-Jan-15 A | 23-Jan-15 A | |
| L05-8206 | Flooring - carpet at corridors | 2 | 0 | 20-Jan-15 A | 21-Jan-15 A | |
| L07-8206 | Flooring - carpet at corridors | 2 | 0 | 22-Jan-15 A | 23-Jan-15 A | |
| L06-8206 | Flooring - carpet at corridors | 2 | 0 | 26-Jan-15 A | 27-Jan-15 A | |
| L09-8206 | Flooring - carpet at corridors | 2 | 0 | 02-Feb-15 A | 03-Feb-15 A | |
| L08-8206 | Flooring - carpet at corridors | 2 | 0 | 04-Feb-15 A | 05-Feb-15 A | |
| L10-8206 | Flooring - carpet at corridors | 2 | 0 | 06-Feb-15 A | 09-Feb-15 A | |
| L11-8206 | Flooring - carpet at corridors | 2 | 0 | 10-Feb-15 A | 11-Feb-15 A | |
| L12-8206 | Flooring - carpet at corridors | 2 | 0 | 11-Feb-15 A | 12-Feb-15 A | |
| L04-8208 | Final Cleaning | 2 | 0 | 13-Feb-15 A | 16-Feb-15 A | |
| L14-8206 | Flooring - carpet at corridors | 2 | 0 | 13-Feb-15 A | 14-Feb-15 A | |
| L15-8206 | Flooring - carpet at corridors | 2 | 0 | 16-Feb-15 A | 17-Feb-15 A | |
| L04-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 17-Feb-15 A | 03-Mar-15 A | |
| L05-8208 | Final Cleaning | 2 | 0 | 17-Feb-15 A | 18-Feb-15 A | |
| L05-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 18-Feb-15 A | 05-Mar-15 A | |
| L16-8206 | Flooring - carpet at corridors | 2 | 0 | 18-Feb-15 A | 19-Feb-15 A | |
| L06-8208 | Final Cleaning | 2 | 0 | 20-Feb-15 A | 25-Feb-15 A | |
| L03-8206 | Flooring - carpet at corridors (N-S leg) | 2 | 0 | 25-Feb-15 A | 25-Feb-15 A | |

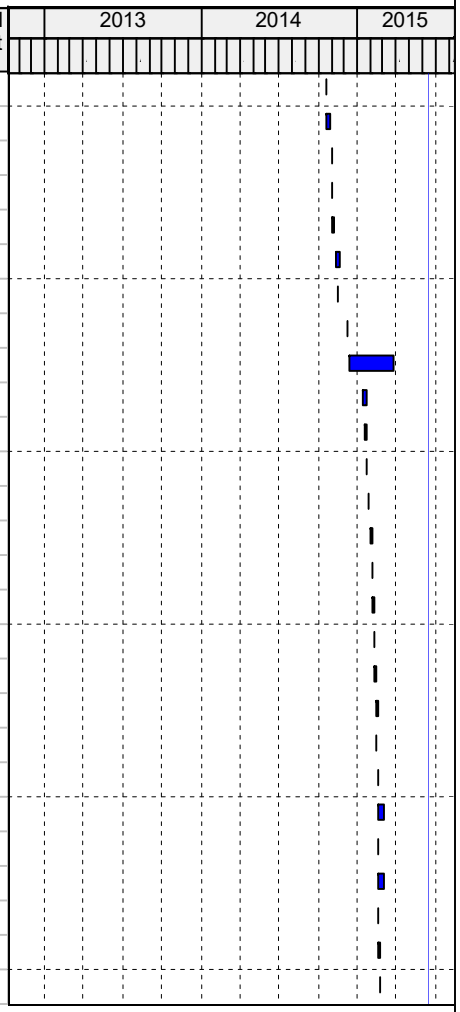



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L06-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 4 | 0 | 25-Feb-15 A | 10-Mar-15 A | |
| L07-8208 | Final Cleaning | 2 | 0 | 27-Feb-15 A | 02-Mar-15 A | |
| L04-8214 | Floor Complete | 0 | 0 | | 03-Mar-15 A | |
| L07-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 05-Mar-15 A | 18-Mar-15 A | |
| L08-8208 | Final Cleaning | 2 | 0 | 05-Mar-15 A | 06-Mar-15 A | |
| L05-8214 | Floor Complete | 0 | 0 | | 05-Mar-15 A | |
| L08-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 06-Mar-15 A | 25-Mar-15 A | |
| L06-8214 | Floor Complete | 0 | 0 | | 10-Mar-15 A | |
| L09-8208 | Final Cleaning | 2 | 0 | 12-Mar-15 A | 13-Mar-15 A | |
| L09-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 12-Mar-15 A | 25-Mar-15 A | |
| L07-8214 | Floor Complete | 0 | 0 | | 18-Mar-15 A | |
| L10-8208 | Final Cleaning | 2 | 0 | 19-Mar-15 A | 20-Mar-15 A | |
| L10-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 9 | 0 | 23-Mar-15 A | 06-Apr-15 A | |
| L11-8208 | Final Cleaning | 2 | 0 | 23-Mar-15 A | 24-Mar-15 A | |
| L11-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 8 | 0 | 24-Mar-15 A | 06-Apr-15 A | |
| L08-8214 | Floor Complete | 0 | 0 | | 25-Mar-15 A | |
| L09-8214 | Floor Complete | 0 | 0 | | 25-Mar-15 A | |
| L12-8208 | Final Cleaning | 2 | 0 | 26-Mar-15 A | 27-Mar-15 A | |
| L12-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 9 | 0 | 31-Mar-15 A | 09-Apr-15 A | |
| L14-8208 | Final Cleaning | 2 | 0 | 31-Mar-15 A | 01-Apr-15 A | |
| L17-8206 | Flooring - carpet at corridors | 2 | 0 | 31-Mar-15 A | 01-Apr-15 A | |
| L14-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 7 | 0 | 06-Apr-15 A | 09-Apr-15 A | |
| L15-8208 | Final Cleaning | 2 | 0 | 06-Apr-15 A | 07-Apr-15 A | |
| L10-8214 | Floor Complete | 0 | 0 | | 06-Apr-15 A | |
| L11-8214 | Floor Complete | 0 | 0 | | 06-Apr-15 A | |
| L15-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 9 | 0 | 08-Apr-15 A | 16-Apr-15 A | |
| L16-8208 | Final Cleaning | 2 | 0 | 09-Apr-15 A | 10-Apr-15 A | |

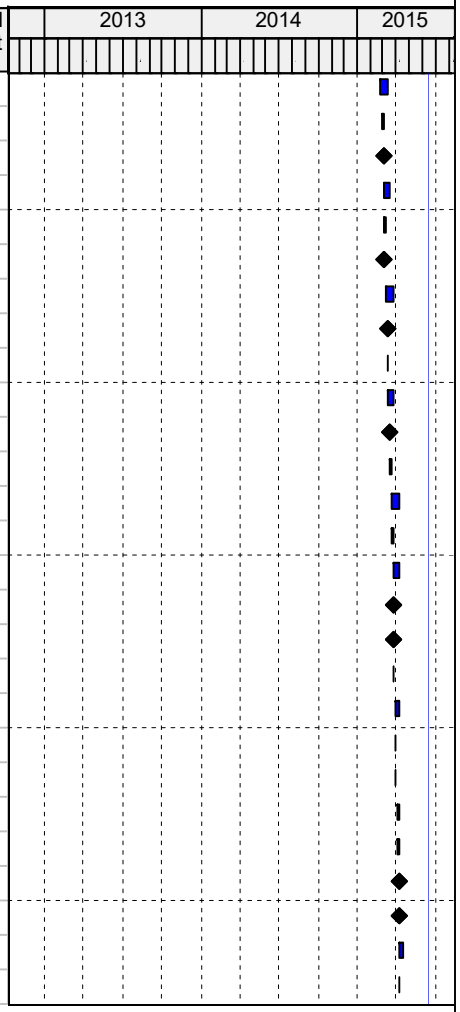



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| L12-8214 | Floor Complete | 0 | 0 | | 09-Apr-15 A | |
| L14-8214 | Floor Complete | 0 | 0 | | 09-Apr-15 A | |
| L16-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 7 | 0 | 10-Apr-15 A | 16-Apr-15 A | |
| L15-8214 | Floor Complete | 0 | 0 | | 16-Apr-15 A | |
| L16-8214 | Floor Complete | 0 | 0 | | 16-Apr-15 A | |
| L03-8208 | Final Cleaning | 2 | 0 | 22-Apr-15 A | 27-Apr-15 A | |
| L03-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 5 | 0 | 29-Apr-15 A | 07-May-15 A | |
| L17-8208 | Final Cleaning | 2 | 0 | 08-May-15 A | 11-May-15 A | |
| L17-8210 | Owner Punchlist (inspect/distribute/correct/back-puncl | 7 | 0 | 12-May-15 A | 15-May-15 A | |
| L17-8214 | Floor Complete | 0 | 0 | | 15-May-15 A | |
| L03-8214 | Floor Complete | 0 | 0 | | 04-Aug-15 | 0 |
| **Mech Penthouse** | | | | | | |
| PH-8100 | PH - Insulation & Vapor Barrier | 5 | 0 | 09-Oct-14 A | 13-Oct-14 A | |
| PH-8102 | PH - Complete GWB Hang / Tape / Finish | 6 | 0 | 14-Oct-14 A | 10-Nov-14 A | |
| PH-8122 | PH - Plumbing Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8110 | PH - HVAC Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8112 | PH - Fire Sprinkler Trim / Finish | 5 | 0 | 24-Nov-14 A | 26-Nov-14 A | |
| PH-8126 | PH - install doors & hardware | 2 | 0 | 24-Nov-14 A | 23-Feb-15 A | |
| PH-8104 | PH - Int Painting [DELETED] | 4 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| PH-8108 | PH - Elec Trim / Finish | 5 | 0 | 01-Dec-14 A | 19-Jan-15 A | |
| PH-8114 | PH - Install Stairs to Roof [DELETED] | 1 | 0 | 01-Dec-14 A | 01-Dec-14 A | |
| PH-8118 | PH - Fire Alarm Trim (speaker/strobe & smoke detecto | 5 | 0 | 01-Dec-14 A | 21-Jan-15 A | |
| PH-8124 | PH - Flooring [DELETED, NIC] | 5 | 0 | 01-Jan-15 A | 01-Jan-15 A | |
| PH-8134 | PH - Final Trims and Touch-Up | 3 | 0 | 16-Mar-15 A | 18-Mar-15 A | |
| PH-8132 | Contractor Punchlist (inspect/distribute/correct/back-pl | 5 | 0 | 20-Apr-15 A | 24-Apr-15 A | |
| PH-8208 | Final Cleaning | 2 | 0 | 27-Apr-15 A | 28-Apr-15 A | |
| PH-8212 | Owner Punchlist (inspect/distribute/correct) | 3 | 0 | 29-Apr-15 A | 01-May-15 A | |

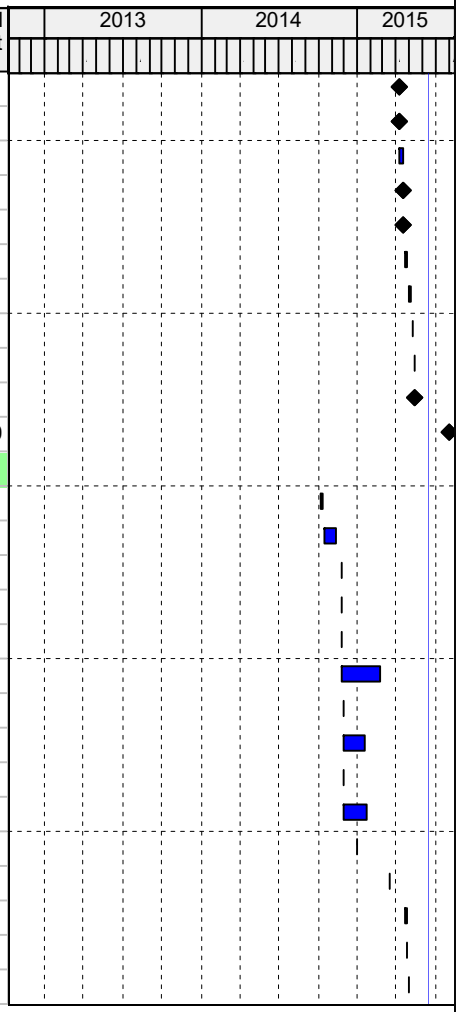



© Oracle Corporation

| Activity ID | Activity Name | Org Dur | Rem Dur | Start | Finish | Total Float |
|---|---|---|---|---|---|---|
| PH-8214 | Penthouse Complete | 0 | 0 | | 01-May-15 A | |
| **Start-Up / Testing / Commissioning** | | | | | | |
| Smoke Control | | | | | | |
| CO-7104 | Fire Alarm/Smoke Control Pre-Functional Testing - Po | 9 | 0 | 18-May-15 A | 05-Jun-15 A | |
| CO-7106 | City of Bellevue Smoke Control Functional Acceptanc | 5 | 5 | 01-Jun-15 A | 19-Jun-15 | 1 |
| CO-7108 | Final Marriott Smoke Control Functional Acceptance T | 2 | 2 | 22-Jun-15 | 23-Jun-15 | 2 |
| Fire Sprinklers | | | | | | |
| CO-7114 | Marriott Fire Sprinkler Funcational Acceptance Testing | 2 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7110 | Fire Sprinkler Pre-Testing (Podium) | 3 | 0 | 26-Mar-15 A | 26-Mar-15 A | |
| CO-7112 | City of Bellevue Fire Sprinkler Final Inspection | 5 | 5 | 01-Jun-15 A | 19-Jun-15 | 1 |
| Fire Alarm | | | | | | |
| CO-7116 | Fire Alarm Pre-Testing (Podium) [DELETED] | 5 | 0 | 01-Mar-15 A | 01-Mar-15 A | |
| CO-7118 | City of Bellevue Fire Alarm Functional Acceptance Tes | 5 | 5 | 01-Jun-15 A | 19-Jun-15 | 1 |
| CO-7120 | Marriott Fire Alarm/Sprinkler Functional Acceptance Te | 2 | 2 | 22-Jun-15 | 23-Jun-15 | 2 |
| Start-Up / Testing / Commissioning | | | | | | |
| CO-7100 | Cx - Start-Up - Garage Exhaust Fan and VFD's | 4 | 0 | 30-Mar-15 A | 02-Apr-15 A | |
| CO-7102 | Cx - DDC Point-To-Point - Garage Exhaust Fans [DEL | 5 | 0 | 01-Apr-15 A | 01-Apr-15 A | |

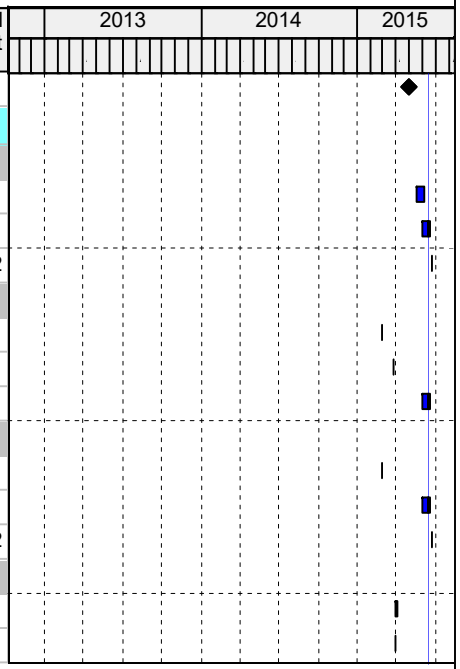



© Oracle Corporation
